



China Harbour Engineering Company Limited

Contract No. HY/2010/02

Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Works

Monthly EM&A Report for December 2015

[01/2016]

	Name	Signature
Prepared & Checked:	Y T Tang	
Reviewed, Approved and Certified:	Echo Leong (ETL)	

Version:	Rev. 0	Date:	14 January 2016
----------	--------	-------	-----------------

Disclaimer

This report is prepared for China Harbour Engineering Company Limited and is given for its sole benefit in relation to and pursuant to Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities-Reclamation Works and may not be disclosed to, quoted to or relied upon by any person other than China Harbour Engineering Company Limited without our prior written consent. No person (other than China Harbour Engineering Company Limited) into whose possession a copy of this report comes may rely on this report without our express written consent and China Harbour Engineering Company Limited may not rely on it for any purpose other than as described above.

AECOM Asia Co. Ltd.
15/F, Grand Central Plaza, Tower 1, 138 Shatin Rural Committee Road, Shatin, NT, Hong Kong
Tel: (852) 3922 9000 Fax: (852) 2317 7609 www.aecom.com

14 January 2016

By Fax (3698 5999) and By Post

Ove Arup & Partners
Chief Resident Engineer's Office
5 Ying Hei Road, Tung Chung, Lantau
Hong Kong

Attention: Mr. Paul Appleton

Dear Sir,

**Re: Agreement No. CE 48/2011 (EP)
Environmental Project Office for the
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities,
and Tuen Mun-Chek Lap Kok Link – Investigation**

**Contract No. HY/2010/02 – HZMB HKBCF – Reclamation Works
Monthly Environmental Monitoring & Audit Report for December 2015**

Reference is made to the Environmental Team's submission of Monthly Environmental Monitoring & Audit Report for December 2015 certified by the ET Leader (ET's ref.: "60249820/C/RMKY16011401" dated 14 January 2016) and provided to us via e-mail on 14 January 2016.

We are pleased to inform you that we have no adverse comment on the captioned report. We write to verify the captioned submission in accordance with Condition 5.4 of EP-353/2009/I and Condition 4.4 of EP-354/2009/D (for TM-CLKL Southern Landfall Reclamation only).

As per Condition 1.7 of EPs, please be reminded to keep in view on the site condition, in particular in the vicinity of Portion B with your on-going surveillance and monitoring.

Thank you very much for your attention and please feel free to contact the undersigned should you require further information.

Yours faithfully,
For and on behalf of
Ramboll Environ Hong Kong Limited



Raymond Dai
Independent Environmental Checker

c.c.	HyD	Mr. Matthew Fung	(By Fax: 3188 6614)
	HyD	Mr. Wai-Ping Lee	(By Fax: 3188 6614)
	AECOM	Ms. Echo Leong	(By Fax: 2317 7609)
	CHEC	Mr. Lim Kim Chuan	(By Fax: 2578 0413)

Internal: DY, YH, LP, CL, ENPO Site

Q:\Projects\HYDZHMBEEM00\02_Proj_Mgt\02_Corr\HYDZHMBEEM00_0_3764L.16.doc

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	3
1 INTRODUCTION	6
1.1 Background	6
1.2 Scope of Report	6
1.3 Project Organization	7
1.4 Summary of Construction Works	7
1.5 Summary of EM&A Programme Requirements	8
2 AIR QUALITY MONITORING	9
2.1 Monitoring Requirements	9
2.2 Monitoring Equipment	9
2.3 Monitoring Locations	9
2.4 Monitoring Parameters, Frequency and Duration	11
2.5 Monitoring Methodology	11
2.6 Monitoring Schedule for the Reporting Month	13
2.7 Results and Observations	13
3 NOISE MONITORING	14
3.1 Monitoring Requirements	14
3.2 Monitoring Equipment	14
3.3 Monitoring Locations	14
3.4 Monitoring Parameters, Frequency and Duration	15
3.5 Monitoring Methodology	15
3.6 Monitoring Schedule for the Reporting Month	15
3.7 Monitoring Results	16
4 WATER QUALITY MONITORING	17
4.1 Monitoring Requirements	17
4.2 Monitoring Equipment	17
4.3 Monitoring Parameters, Frequency and Duration	17
4.4 Monitoring Locations	18
4.5 Monitoring Methodology	19
4.6 Monitoring Schedule for the Reporting Month	20
5 DOLPHIN MONITORING	23
5.1 Monitoring Requirements	23
5.2 Monitoring Equipment	23
5.3 Monitoring Frequency and Conditions	23
5.4 Monitoring Methodology and Location	23
5.5 Monitoring Procedures	25
5.6 Monitoring Schedule for the Reporting Month	25
5.7 Results and Observations	25
6 ENVIRONMENTAL SITE INSPECTION AND AUDIT	28
6.1 Site Inspection	28
6.2 Advice on the Solid and Liquid Waste Management Status	30
6.3 Environmental Licenses and Permits	31
6.4 Implementation Status of Environmental Mitigation Measures	32
6.5 Summary of Exceedances of the Environmental Quality Performance Limit	35
6.6 Summary of Complaints, Notification of Summons and Successful Prosecutions	35
7 FUTURE KEY ISSUES	37
7.1 Construction Programme for the Coming Months	37
7.2 Key Issues for the Coming Month	38
7.3 Monitoring Schedule for the Coming Month	38
8 CONCLUSIONS AND RECOMMENDATIONS	39

8.1	Conclusions	39
8.2	Recommendations	40

List of Tables

Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Locations of Impact Air Quality Monitoring Stations
Table 2.3	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.4	Summary of 1-hour TSP Monitoring Results in the Reporting Period
Table 2.5	Summary of 24-hour TSP Monitoring Results in the Reporting Period
Table 3.1	Noise Monitoring Equipment
Table 3.2	Locations of Impact Noise Monitoring Stations
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Summary of Construction Noise Monitoring Results in the Reporting Period
Table 4.1	Water Quality Monitoring Equipment
Table 4.2	Impact Water Quality Monitoring Parameters and Frequency
Table 4.3	Impact Water Quality Monitoring Stations
Table 4.4	Laboratory Analysis for Suspended Solids
Table 4.5	Summary of Water Quality Exceedances
Table 5.1	Dolphin Monitoring Equipment
Table 5.2	Impact Dolphin Monitoring Line Transect Co-ordinates (Provided by AFCD)
Table 5.3	Impact Dolphin Monitoring Survey Effort Summary, Effort by Area and Beaufort Sea State
Table 5.4	Impact Dolphin Monitoring Survey Details December 2015
Table 5.5	The Encounter Rate of Number of Dolphin Sightings & Total Number of Dolphins per Area [^]
Table 6.1	Summary of Environmental Licensing and Permit Status

Figures

Figure 1	General Project Layout Plan
Figure 2	Impact Air Quality and Noise Monitoring Stations and Wind Station
Figure 3	Impact Water Quality Monitoring Stations
Figure 4	Impact Dolphin Monitoring Line Transect Layout Map
Figure 5	Impact Dolphin Monitoring Survey Efforts and Sightings in December 2015
Figure 6	Environmental Complaint Handling Procedures

List of Appendices

Appendix A	Project Organization for Environmental Works
Appendix B	Three Month Rolling Construction Programmes
Appendix C	Implementation Schedule of Environmental Mitigation Measures (EMIS)
Appendix D	Summary of Action and Limit Levels
Appendix E	Calibration Certificates of Monitoring Equipments
Appendix F	EM&A Monitoring Schedules
Appendix G	Impact Air Quality Monitoring Results and their Graphical Presentation
Appendix H	Meteorological Data for Monitoring Periods on Monitoring Dates in December 2015
Appendix I	Impact Construction Noise Monitoring Results and their Graphical Presentation
Appendix J	Impact Water Quality Monitoring Results and their Graphical Presentation
Appendix K	Impact Dolphin Monitoring Survey Sighting Summary
Appendix L	Event Action Plan
Appendix M	Monthly Summary of Waste Flow Table
Appendix N	Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

EXECUTIVE SUMMARY

Contract No. HY/2010/02 – Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Work (here below, known as “the Project”) mainly comprises reclamation at the northeast of the Hong Kong International Airport of an area of about 130-hectare for the construction of an artificial island for the development of the Hong Kong Boundary Crossing Facilities (HKBCF), and about 19-hectare for the southern landfall of the Tuen Mun - Chek Lap Kok Link (TMCLKL). It is a designated project and is governed by the current permits for the Project, i.e. the amended Environmental Permits (EPs) issued on 17 July 2015 (EP-353/2009/I) and 13 March 2015 (EP-354/2009/D) (for TMCLKL Southern Landfall Reclamation only).

Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the consultants for the design and construction assignment for the Project’s reclamation works (i.e. the Engineer for the Project).

China Harbour Engineering Company Limited (CHEC) was awarded by HyD as the Contractor to undertake the construction work of the Project.

Ramboll Environ Hong Kong Limited. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project.

AECOM Asia Co. Ltd. (AECOM) was appointed by CHEC to undertake the role of Environmental Team for the Project for carrying out the environmental monitoring and audit (EM&A) works.

The construction phase of the Project under the EPs was commenced on 12 March 2012 and will be tentatively completed by early Year 2016. The EM&A programme, including air quality, noise, water quality and dolphin monitoring and environmental site inspections, was commenced on 12 March 2012.

This report documents the findings of EM&A works conducted in the period between 1 and 31 December 2015. As informed by the Contractor, major activities in the reporting period were:-

Marine-base

- Rock fill
- Conforming Sloping Seawalls
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Rubble Mound Seawall

Land-base

- Earthwork fill
- Surcharge removal & laying
- Deep Cement Mixing
- Removal of Temporary Seawall
- Vertical Band Drains
- Installations of Precast Culverts except sloping outfalls
- Geotechnical Instrumentation Works
- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Maintenance of Temporary Marine Access at Works Area WA2

A summary of monitoring and audit activities conducted in the reporting period is listed below:

24-hour Total Suspended Particulates (TSP) monitoring	6 sessions
1-hour TSP monitoring	6 sessions
Noise monitoring	5 sessions
Impact water quality monitoring	13 sessions
Impact dolphin monitoring	2 surveys
Joint Environmental site inspection	5 sessions

Breaches of Action and Limit Levels for Air Quality

For impact air quality monitoring, no exceedance of 1-Hour TSP or 24-Hour TSP was recorded at all monitoring stations in the reporting month.

Breaches of Action and Limit Levels for Noise

For construction noise, no exceedance was recorded at all monitoring stations in the reporting month.

Breaches of Action and Limit Levels for Water Quality

One (1) action level impact water quality monitoring exceedance at monitoring station IS(Mf)11 has been recorded on 28 December 2015 during flood tide. After investigation, there is no adequate information to conclude the recorded exceedance is related to this Contract.

Impact Dolphin Monitoring

A total of two sightings were made, both are “on effort” sighting and were recorded on the 1 December 2015. Details are summarised and plotted in Appendix K and Figure 5c, respectively. The first group sighted on 1 December 2015 contained 3 individuals, second group contained 8 individuals. No calf was observed in December 2015

Behaviour: On 1 December 2015, the first group was travelling and the second group was engaged in multiple behaviours, i.e., feeding and active surfacing.

Complaint, Notification of Summons and Successful Prosecution

A water quality complaint was referred to the ENPO at 10:22 am on the 4 December 2015 by EPD; ENPO referred this complaint to this Contract on the same day. With referred to the information provided by ENPO, EPD has contacted the complainant, and obtained the additional information from the complainant and it is suspected that the incident happened in the afternoon on 28 November 2015. A video was provided by the complainant who shows that turbid water behind a barge, the incident is suspected to be happened in the afternoon on 28 November 2015. After investigation, it is considered not related to this Contract.

No notification of summons or prosecution was received in the reporting period.

Reporting Change

There was no reporting change required in the reporting period.

Future Key Issues

Key issues to be considered in the coming month included:

- Site runoff should be properly collected and treated prior to discharge;
- Minimize loss of sediment from filling works;
- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities;
- Exposed surfaces/soil stockpiles should be properly treated to avoid generation of silty surface run-off during rainstorm;
- Regular review and maintenance of wheel washing facilities provided at all site entrances/exits;
- Conduct regular inspection of various working machineries and vessels within works areas to avoid any dark smoke emission;
- Suppress dust generated from work processes with use of bagged cements, earth movements, excavation activities, exposed surfaces/soil stockpiles and haul road traffic;
- Quieter powered mechanical equipment should be used;
- Provision of proper and effective noise control measures for operating equipment and machinery on-site, such as erection of movable noise barriers or enclosure for noisy plants;
- Closely check and replace the sound insulation materials regularly;
- Better scheduling of construction works to minimize noise nuisance;
- Properly store and label oil drums and chemical containers placed on site;
- Proper chemicals, chemical wastes and wastes management;
- Maintenance works should be carried out within roofed, paved and confined areas;

Contract No. HY/2010/02

Hong Kong-Zhuhai-Macao Bridge

Hong Kong Boundary Crossing Facilities – Reclamation Works Monthly EM&A Report for December 2015

- Collection and segregation of construction waste and general refuse on land and in the sea should be carried out properly and regularly; and
- Proper protection and regular inspection of existing trees, transplanted/retained trees.
- Control night-time lighting and glare by hooding all lights.
- Regular review and provide maintenance to dust control measures such as sprinkler system.

1 INTRODUCTION

1.1 Background

- 1.1.1 Contract No. HY/2010/02 – Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Work (here below, known as “the Project”) mainly comprises reclamation at the northeast of the Hong Kong International Airport of an area of about 130-hectare for the construction of an artificial island for the development of the Hong Kong Boundary Crossing Facilities (HKBCF), and about 19-hectare for the southern landfall of the Tuen Mun - Chek Lap Kok Link (TMCLKL).
- 1.1.2 The environmental impact assessment (EIA) reports (Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities – EIA Report (Register No. AEIAR-145/2009) (HKBCFEIA) and Tuen Mun – Chek Lap Kok Link – EIA Report (Register No. AEIAR-146/2009) (TMCLKLEIA), and their environmental monitoring and audit (EM&A) Manuals (original EM&A Manuals), for the Project were approved by Environmental Protection Department (EPD) in October 2009.
- 1.1.3 EPD subsequently issued the Environmental Permit (EP) for HKBCF in November 2009 (EP-353/2009) and the Variation of Environmental Permit (VEP) in June 2010 (EP-353/2009/A), November 2010 (EP-353/2009/B), November 2011 (EP-353/2009/C), March 2012 (EP-353/2009/D), October 2012 (EP-353/2009/E), April 2013 (EP-353/2009/F), August 2013 (EP-353/2009/G), January 2015 (EP-353/2009/H) and July 2015 (EP-353/2009/I). Similarly, EPD issued the Environmental Permit (EP) for TMCLKL in November 2009 (EP-354/2009) and the Variation of Environmental Permit (VEP) in December 2010 (EP-354/2009/A), January 2014 (EP-354/2009/B), December 2014 (EP-354/2009/C) and March 2015 (EP-354/2009/D).
- 1.1.4 The Project is a designated project and is governed by the current permits for the Project, i.e. the amended EPs issued on 17 July 2015 (EP-353/2009/I) and 13 March 2015 (EP-354/2009/D) (for TMCLKL Southern Landfall Reclamation only).
- 1.1.5 A Project Specific EM&A Manual, which included all project-relation contents from the original EM&A Manuals for the Project, was issued in May 2012.
- 1.1.6 Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the consultants for the design and construction assignment for the Project’s reclamation works (i.e. the Engineer for the Project).
- 1.1.7 China Harbour Engineering Company Limited (CHEC) was awarded by HyD as the Contractor to undertake the construction work of the Project.
- 1.1.8 Ramboll Environ Hong Kong Limited. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project.
- 1.1.9 AECOM Asia Co. Ltd. (AECOM) was appointed by CHEC to undertake the role of Environmental Team for the Project for carrying out the EM&A works.
- 1.1.10 The construction phase of the Project under the EPs was commenced on 12 March 2012 and will be tentatively completed by early Year 2016.
- 1.1.11 According to the Project Specific EM&A Manual, there is a need of an EM&A programme including air quality, noise, water quality and dolphin monitoring and environmental site inspections. The EM&A programme of the Project commenced on 12 March 2012.

1.2 Scope of Report

- 1.2.1 This is the forty-sixth monthly EM&A Report under the Contract No.HY/2010/02 Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Works. This report presents a summary of the environmental monitoring and audit works, list of activities and mitigation measures proposed by the ET for the Project in December 2015.

1.3 Project Organization

1.3.1 The project organization structure is shown in Appendix A. The key personnel contact names and numbers are summarized in Table 1.1.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Engineer's Representative (ER) (Ove Arup & Partners Hong Kong Limited)	Chief Resident Engineer	Paul Appleton	3698 5889	2698 5999
	IEC / ENPO (Ramboll Environ Hong Kong Limited)	Independent Environmental Checker	Raymond Dai	3465 2888
Contractor (China Harbour Engineering Company Limited)	Environmental Project Office Leader	Y. H. Hui	3547 2133	3465 2899
	Environmental Officer	Louie Chan	36932254	2578 0413
ET (AECOM Asia Company Limited)	24-hour Hotline	Alan C.C. Yeung	9448 0325	--
	ET Leader	Echo Leong	3922 9280	2317 7609

1.4 Summary of Construction Works

1.4.1 The construction phase of the Project under the EP commenced on 12 March 2012.

1.4.2 As informed by the Contractor, details of the major works carried out in this reporting period are listed below:-

Marine-base

- Rock fill
- Conforming Sloping Seawalls
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Rubble Mound Seawall

Land-base

- Earthwork fill
- Surcharge removal & laying
- Deep Cement Mixing
- Removal of Temporary Seawall
- Vertical Band Drains
- Installations of Precast Culverts except sloping outfalls
- Geotechnical Instrumentation Works
- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Maintenance of Temporary Marine Access at Works Area WA2

1.4.3 The 3-month rolling construction programme of the Project is shown in Appendix B.

1.4.4 The general layout plan of the Project site showing the detailed works areas is shown in Figure 1.

1.4.5 The environmental mitigation measures implementation schedule are presented in Appendix C.

1.5 Summary of EM&A Programme Requirements

1.5.1 The EM&A programme required environmental monitoring for air quality, noise, water quality, marine ecology and environmental site inspections for air quality, noise, water quality, waste management, marine ecology, and landscape and visual impact. The EM&A requirements for each parameter described in the following sections include:-

- All monitoring parameters;
- Monitoring schedules for the reporting month and forthcoming month;
- Action and Limit levels for all environmental parameters;
- Event / Action Plan;
- Environmental mitigation measures, as recommended in the Project EIA reports; and
- Environmental requirement in contract documents.

2 AIR QUALITY MONITORING

2.1 Monitoring Requirements

2.1.1 In accordance with the Project Specific EM&A Manual, baseline 1-hour and 24-hour Total Suspended Particulates (TSP) levels at 4 air quality monitoring stations were established. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days, while impact 24-hour TSP monitoring was carried out for at least once every 6 days. The Action and Limit level of the air quality monitoring is provided in Appendix D.

2.2 Monitoring Equipment

2.2.1 24-hour TSP air quality monitoring was performed using High Volume Sampler (HVS) located at each designated monitoring station. The HVS meets all the requirements of the Project Specific EM&A Manual. Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. Brand and model of the equipment is given in Table 2.1.

Table 2.1 Air Quality Monitoring Equipment

Equipment	Brand and Model
Portable direct reading dust meter (1-hour TSP)	Sibata Digital Dust Monitor (Model No. LD-3 and LD-3B)
High Volume Sampler (24-hour TSP)	Tisch Environmental Mass Flow Controlled Total Suspended Particulate (TSP) High Volume Air Sampler (Model No. TE-5170)

2.3 Monitoring Locations

2.3.1 Monitoring locations AMS2 and AMS7 were set up at the proposed locations in accordance with Project Specific EM&A Manual. For AMS6 (Dragonair/CNAC (Group) Building), permission on setting up and carrying out impact monitoring works was sought, however, access to the premise has not been granted yet on this report issuing date. For monitoring location AMS3 (Ho Yu College), as proposed in the Project Specific EM&A Manual, approval for carrying out impact monitoring could not be obtained from the principal of the school. Permission on setting up and carrying out impact monitoring works at nearby sensitive receivers, like Caribbean Coast and Coastal Skyline, was also sought. However, approvals for carrying out impact monitoring works within their premises were not obtained. Impact air quality monitoring was conducted at site boundary of the site office area in Works Area WA2 (AMS3B) respectively. Same baseline and Action Level for air quality, as derived from the baseline monitoring data recorded at Ho Yu College, was adopted for this alternative air quality location.

2.3.2 It was observed that a tree near AMS3B may affect the wind flow around the HVS located at AMS3B. With no further comment received from IEC, the HVS at AMS3B has been relocated on 8 September 2014 to slightly more than 2 meters separation from it, measured horizontally. Same baseline and Action Level for air quality, as derived from the baseline monitoring data recorded at Ho Yu College, was adopted for this alternative air quality location.

2.3.3 Reference is made to ET’s proposal of the omission of air monitoring station (AMS 6) dated on 1 November 2012 and EPD’s letter dated on 19 November 2012 regarding the conditional approval of the proposed omission of air monitoring station (AMS 6) for Contract No. HY/2010/02. The aforesaid omission of Monitoring Station AMS6 is effective since 19 November 2012.

2.3.4 As informed by the premises owner of (AMS7A) - Chu Kong Air-Sea Union Transportation Co. LTD would not grant us the permission to install air quality monitoring equipment (High volume sampler) and conduct 1-hour TSP/24 hour TSP monitoring at the premises of Chu Kong Air-Sea Union Transportation Co. LTD after December 2015. In order to fulfil the EM&A requirement of this Contract, as permission to conduct impact air quality monitoring at the premise of Hong Kong SkyCity Marriott Hotel has been granted in December 2015, ET proposed relocation of air quality monitoring station (AMS7A) on 15 December 2015, with no further comment received from IEC on 15 December 2015

and no particular comment received from EPD on 21 December 2015, the impact air quality monitoring station AMS7A (Chu Kong Air-Sea Union Transportation Company Limited) has been relocated to AMS7 (Hong Kong SkyCity Marriott Hotel) on 30 December 2015. The impact air quality monitoring for December 2015 was conducted before the relocation of AQM Station from AMS7A to AMS7. Action Level for air quality, as derived from the baseline monitoring data recorded at Hong Kong SkyCity Marriott Hotel will be adopted for this air quality monitoring location.

- 2.3.5 Figure 2 shows the locations of monitoring stations. Table 2.2 describes the details of the monitoring stations.

Table 2.2 Locations of Impact Air Quality Monitoring Stations

Monitoring Station	Location	Description
AMS2	Tung Chung Development Pier	Rooftop of the premise
AMS3B	Site Boundary of Site Office Area at Works Area WA2	On ground at the area boundary
AMS6*	Dragonair/CNAC (Group) Building	On ground at boundary of the premise
AMS7A	Chu Kong Air-Sea Union Transportation Company Limited	On ground at boundary of the premise

*Remarks: Reference is made to EPD conditional approval of the omission of air monitoring station (AMS 6) for the project. The omission will be effective on 19 November 2012.

2.4 Monitoring Parameters, Frequency and Duration

2.4.1 Table 2.3 summarizes the monitoring parameters, frequency and duration of impact TSP monitoring.

Table 2.3 Air Quality Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
1-hour TSP	Three times every 6 days while the highest dust impact was expected
24-hour TSP	Once every 6 days

2.5 Monitoring Methodology

2.5.1 24-hour TSP Monitoring

- (a) The HVS was installed in the vicinity of the air sensitive receivers. The following criteria were considered in the installation of the HVS.
 - (i) A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
 - (ii) No two samplers should be placed less than 2 meters apart.
 - (iii) The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
 - (iv) A minimum of 2 meters separation from walls, parapets and penthouse for rooftop sampler.
 - (v) A minimum of 2 meters separation from any supporting structure, measured horizontally is required.
 - (vi) No furnace or incinerator flues nearby.
 - (vii) Airflow around the sampler was unrestricted.
 - (viii) Permission was obtained to set up the samplers and access to the monitoring stations.
 - (ix) A secured supply of electricity was obtained to operate the samplers.
 - (x) The sampler was located more than 20 meters from any dripline.
 - (xi) Any wire fence and gate, required to protect the sampler, did not obstruct the monitoring process.
 - (xii) Flow control accuracy was kept within $\pm 2.5\%$ deviation over 24-hour sampling period.
- (b) Preparation of Filter Papers
 - (i) Glass fibre filters, G810 were labelled and sufficient filters that were clean and without pinholes were selected.
 - (ii) All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ± 3 °C; the relative humidity (RH) was < 50% and not variable by more than $\pm 5\%$. A convenient working RH was 40%.

- (iii) All filter papers were prepared and analysed by ALS Technichem (HK) Pty Ltd., which is a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes.
- (c) Field Monitoring
- (i) The power supply was checked to ensure the HVS works properly.
 - (ii) The filter holder and the area surrounding the filter were cleaned.
 - (iii) The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
 - (iv) The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
 - (v) The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied was sufficient to avoid air leakage at the edges.
 - (vi) Then the shelter lid was closed and was secured with the aluminum strip.
 - (vii) The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
 - (viii) A new flow rate record sheet was set into the flow recorder.
 - (ix) On site temperature and atmospheric pressure readings were taken and the flow rate of the HVS was checked and adjusted at around 1.1 m³/min, and complied with the range specified in the updated EM&A Manual (i.e. 0.6-1.7 m³/min).
 - (x) The programmable digital timer was set for a sampling period of 24 hrs, and the starting time, weather condition and the filter number were recorded.
 - (xi) The initial elapsed time was recorded.
 - (xii) At the end of sampling, on site temperature and atmospheric pressure readings were taken and the final flow rate of the HVS was checked and recorded.
 - (xiii) The final elapsed time was recorded.
 - (xiv) The sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
 - (xv) It was then placed in a clean plastic envelope and sealed.
 - (xvi) All monitoring information was recorded on a standard data sheet.
 - (xvii) Filters were then sent to ALS Technichem (HK) Pty Ltd. for analysis.
- (d) Maintenance and Calibration
- (i) The HVS and its accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
 - (ii) 5-point calibration of the HVS was conducted using TE-5025A Calibration Kit prior to the commencement of baseline monitoring. Bi-monthly 5-point calibration of the HVS will be carried out during impact monitoring.
 - (iii) Calibration certificate of the HVSs are provided in Appendix E.

2.5.2 1-hour TSP Monitoring

(a) Measuring Procedures

The measuring procedures of the 1-hour dust meter were in accordance with the Manufacturer's Instruction Manual as follows:-

- (i) Turn the power on.
- (ii) Close the air collecting opening cover.
- (iii) Push the "TIME SETTING" switch to [BG].
- (iv) Push "START/STOP" switch to perform background measurement for 6 seconds.
- (v) Turn the knob at SENSI ADJ position to insert the light scattering plate.
- (vi) Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
- (vii) Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- (viii) Pull out the knob and return it to MEASURE position.
- (ix) Push the "TIME SETTING" switch the time set in the display to 3 hours.
- (x) Lower down the air collection opening cover.
- (xi) Push "START/STOP" switch to start measurement.

(b) Maintenance and Calibration

- (i) The 1-hour TSP meter was calibrated at 1-year intervals against a continuous particulate TEOM Monitor, Series 1400ab. Calibration certificates of the Laser Dust Monitors are provided in Appendix E.
- (ii) 1-hour validation checking of the TSP meter against HVS is carried out on half-year basis at the air quality monitoring locations.

2.6 Monitoring Schedule for the Reporting Month

2.6.1 The schedule for air quality monitoring in December 2015 is provided in Appendix F.

2.7 Results and Observations

2.7.1 The monitoring results for 1-hour TSP and 24-hour TSP are summarized in Table 2.4 and 2.5 respectively. Detailed impact air quality monitoring results are presented in Appendix G.

Table 2.4 Summary of 1-hour TSP Monitoring Results in the Reporting Period

	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AMS2	75	72-82	374	500
AMS3B	74	70-80	368	500
AMS7A	78	72-82	370	500

Table 2.5 Summary of 24-hour TSP Monitoring Results in the Reporting Period

	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AMS2	60	42-97	176	260
AMS3B	48	32-63	167	260
AMS7A	53	42-65	183	260

2.7.2 The event action plan is annexed in Appendix L.

2.7.3 Meteorological information collected from the wind station during the monitoring periods on the monitoring dates, as shown in Figure 2, including wind speed and wind direction, is annexed in Appendix H.

3 NOISE MONITORING

3.1 Monitoring Requirements

3.1.1 In accordance with the Project Specific EM&A Manual, impact noise monitoring was conducted for at least once per week during the construction phase of the Project. The Action and Limit level of the noise monitoring is provided in Appendix D.

3.2 Monitoring Equipment

3.2.1 Noise monitoring was performed using sound level meter at each designated monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment is given in Table 3.1.

Table 3.1 Noise Monitoring Equipment

Equipment	Brand and Model
Integrated Sound Level Meter	Rion NL-31 & B&K2238
Acoustic Calibrator	Rion NC-73 & B&K 4231

3.3 Monitoring Locations

3.3.1 Monitoring locations NMS2 was set up at the proposed locations in accordance with Project Specific EM&A Manual. However, for monitoring location NMS3 (Ho Yu College), as proposed in the Project Specific EM&A Manual, approval for carrying out impact monitoring could not be obtained from the principal of the school. Permission on setting up and carrying out impact monitoring works at nearby sensitive receivers, like Caribbean Coast and Coastal Skyline, was also sought. However, approvals for carrying out impact monitoring works within their premises were not obtained. Impact noise monitoring was conducted at site boundary of the site office area in Works Area WA2 (NMS3B) respectively. Same baseline noise level (as derived from the baseline monitoring data recorded at Ho Yu College) and Limit Level were adopted for this alternative noise monitoring location.

3.3.2 Figure 2 shows the locations of the monitoring stations. Table 3.2 describes the details of the monitoring stations.

Table 3.2 Locations of Impact Noise Monitoring Stations

Monitoring Station	Location	Description
NMS2	Seaview Crescent Tower 1	Free-field on the rooftop of the premise
NMS3B	Site Boundary of Site Office Area at Works Area WA2	Free-field on ground at the area boundary.

3.4 Monitoring Parameters, Frequency and Duration

3.4.1 Table 3.3 summarizes the monitoring parameters, frequency and duration of impact noise monitoring.

Table 3.3 Noise Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays (Monday to Saturday). L_{eq} , L_{10} and L_{90} would be recorded.	At least once per week

3.5 Monitoring Methodology

3.5.1 Monitoring Procedure

- (a) The sound level meter was set on a tripod at a height of 1.2 m above the ground for free-field measurements at NMS2. A correction of +3 dB(A) shall be made to the free field measurements.
- (b) All measurement at NMS3B were free field measurements in the reporting month at NMS3B. A correction of +3 dB(A) shall be made to the free field measurements.
- (c) The battery condition was checked to ensure the correct functioning of the meter.
- (d) Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:-
 - (i) frequency weighting: A
 - (ii) time weighting: Fast
 - (iii) time measurement: $L_{eq(30-minutes)}$ during non-restricted hours i.e. 07:00 – 1900 on normal weekdays.
- (e) Prior to and after each noise measurement, the meter was calibrated using the acoustic calibrator for 94dB(A) at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- (f) During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- (g) Noise measurement was paused during periods of high intrusive noise (e.g. dog barking, helicopter noise) if possible. Observations were recorded when intrusive noise was unavoidable.
- (h) Noise monitoring was cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind with gusts exceeding 10m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.5.2 Maintenance and Calibration

- (a) The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
- (b) The meter and calibrator were sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- (c) Calibration certificates of the sound level meters and acoustic calibrators are provided in Appendix E.

3.6 Monitoring Schedule for the Reporting Month

3.6.1 The schedule for construction noise monitoring in December 2015 is provided in Appendix F.

3.7 Monitoring Results

3.7.1 The monitoring results for construction noise are summarized in Table 3.4 and the monitoring data is provided in Appendix I.

Table 3.4 Summary of Construction Noise Monitoring Results in the Reporting Period

	Average, dB(A), L_{eq} (30 mins)	Range, dB(A), L_{eq} (30 mins)	Limit Level, dB(A), L_{eq} (30 mins)
NMS2	67	63-68*	75
NMS3B	67	64-68*	70/65^

*+3dB(A) Façade correction included

^ Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

- 3.7.2 No Action or Limit Level Exceedance of construction noise was recorded in the reporting month.
- 3.7.3 Major noise sources during the noise monitoring included construction activities of the Project, construction activities by other contracts and nearby traffic noise.
- 3.7.4 The event action plan is annexed in Appendix L.

4 WATER QUALITY MONITORING

4.1 Monitoring Requirements

4.1.1 Impact water quality monitoring was carried out to ensure that any deterioration of water quality was detected, and that timely action was taken to rectify the situation. For impact water quality monitoring, measurements were taken in accordance with the Project Specific EM&A Manual. Appendix D shows the established Action/Limit Levels for the environmental monitoring works.

4.2 Monitoring Equipment

4.2.1 Table 4.1 summarises the equipment used in the impact water quality monitoring programme.

Table 4.1 Water Quality Monitoring Equipment

Equipment	Brand and Model
Dissolved Oxygen (DO) and Temperature Meter, Salinity Meter and Turbidity Meter	YSI Model 6820
pH Meter	YSI Model 6820 or Thermo Orion 230A+
Positioning Equipment	JRC DGPS 224 Model JLR-4341 with J-NAV 500 Model NWZ4551
Water Depth Detector	Eagle Cuda-168 and Lowrance x-4
Water Sampler	Kahlsio Water Sampler (Vertical) 2.2 L with messenger

4.3 Monitoring Parameters, Frequency and Duration

4.3.1 Table 4.2 summarises the monitoring parameters, frequency and monitoring depths of impact water quality monitoring as required in the Project Specific EM&A Manual.

Table 4.2 Impact Water Quality Monitoring Parameters and Frequency

Monitoring Stations	Parameter, unit	Frequency	No. of depth
<p><i>Impact Stations:</i> IS5, IS(Mf)6, IS7, IS8, IS(Mf)9, IS10, IS(Mf)11, IS(Mf)16, IS17</p> <p><i>Control/Far Field Stations:</i> CS(Mf)3, CS(Mf)5, CS4, CS6, CSA</p> <p><i>Sensitive Receiver Stations:</i> SR3-SR7, SR10A&SR10B</p>	<ul style="list-style-type: none"> • Depth, m • Temperature, °C • Salinity, ppt • Dissolved Oxygen (DO), mg/L • DO Saturation, % • Turbidity, NTU • pH • Suspended Solids (SS), mg/L 	<p>Three times per week during mid-ebb and mid-flood tides (within ± 1.75 hour of the predicted time)</p>	<p>3 (1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth is less than 6 m, in which case the mid-depth station may be omitted. Should the water depth be less than 3 m, only the mid-depth station will be monitored).</p>

4.4 Monitoring Locations

- 4.4.1 In accordance with the Project Specific EM&A Manual, twenty-one stations (9 Impact Stations, 7 Sensitive Receiver Stations and 5 Control/Far Field Stations) were designated for impact water quality monitoring. The nine Impact Stations (IS) were chosen on the basis of their proximity to the reclamation and thus the greatest potential for water quality impacts, the seven Sensitive Receiver Stations (SR) were chosen as they are close to the key sensitive receives and the five Control/ Far Field Stations (CS) were chosen to facilitate comparison of the water quality of the IS stations with less influence by the Project/ ambient water quality conditions.
- 4.4.2 Due to safety concern and topographical condition of the original locations of SR4 and SR10B, alternative impact water quality monitoring stations, naming as SR4 (N) and SR10B (N), were adopted, which are situated in vicinity of the original impact water quality monitoring stations (SR4 and SR10B) and could be reachable.
- 4.4.3 Same baseline and Action Level for water quality, as derived from the baseline monitoring data recorded, were adopted for these alternative impact water quality monitoring stations.
- 4.4.4 The locations of these monitoring stations are summarized in Table 4.3 and depicted in Figure 3.

Table 4.3 Impact Water Quality Monitoring Stations

Station	Description	East	North
IS5	Impact Station (Close to HKBCF construction site)	811579	817106
IS(Mf)6	Impact Station (Close to HKBCF construction site)	812101	817873
IS7	Impact Station (Close to HKBCF construction site)	812244	818777
IS8	Impact Station (Close to HKBCF construction site)	814251	818412
IS(Mf)9	Impact Station (Close to HKBCF construction site)	813273	818850
IS10	Impact Station (Close to HKBCF construction site)	812577	820670
IS(Mf)11	Impact Station (Close to HKBCF construction site)	813562	820716
IS(Mf)16	Impact Station (Close to HKBCF construction site)	814328	819497
IS17	Impact Station (Close to HKBCF construction site)	814539	820391
SR3	Sensitive receivers (San Tau SSSI)	810525	816456
SR4(N)	Sensitive receivers (Tai Ho)	814705	817859
SR5	Sensitive receivers (Artificial Reef in NE Airport)	811489	820455
SR6	Sensitive receivers (Sha Chau and Lung Kwu Chau Marine Park)	805837	821818
SR7	Sensitive receivers (Tai Mo Do)	814293	821431
SR10A	Sensitive receivers (Ma Wan FCZ)1	823741	823495
SR10B(N)	Sensitive receivers (Ma Wan FCZ)2	823683	823187
CS(Mf)3	Control Station	809989	821117
CS(Mf)5	Control Station	817990	821129
CS4	Control Station	810025	824004
CS6	Control Station	817028	823992
CSA	Control Station	818103	823064

4.5 Monitoring Methodology

4.5.1 Instrumentation

- (a) The in-situ water quality parameters, viz. dissolved oxygen, temperature, salinity, turbidity and pH, were measured by multi-parameter meters (i.e. Model YSI 6820 CE-C-M-Y) and pH meter (i.e. Thermo Orion 230A+) respectively.

4.5.2 Operating/Analytical Procedures

- (a) Digital Differential Global Positioning Systems (DGPS) were used to ensure that the correct location was selected prior to sample collection.
- (b) Portable, battery-operated echo sounders were used for the determination of water depth at each designated monitoring station.
- (c) All in-situ measurements were taken at 3 water depths, 1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth was less than 6 m, in which case the mid-depth station was omitted. Should the water depth be less than 3 m, only the mid-depth station was monitored.
- (d) At each measurement/sampling depth, two consecutive in-situ monitoring (DO concentration and saturation, temperature, turbidity, pH, salinity) and water sample for SS. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of DO or turbidity parameters was more than 25% of the value of the first reading, the reading was discarded and further readings were taken.
- (e) Duplicate samples from each independent sampling event were collected for SS measurement. Water samples were collected using the water samplers and the samples were stored in high-density polythene bottles. Water samples collected were well-mixed in the water sampler prior to pre-rinsing and transferring to sample bottles. Sample bottles were pre-rinsed with the same water samples. The sample bottles were then be packed in cool-boxes (cooled at 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. for the analysis of suspended solids concentrations. The laboratory determination work would be started within 24 hours after collection of the water samples. ALS Technichem (HK) Pty Ltd. is a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes. For QA/QC procedures, one duplicate samples of every batch of 20 samples was analyzed.
- (f) The analysis method and reporting and detection limit for SS is shown in Table 4.4.

Table 4.4 Laboratory Analysis for Suspended Solids

Parameters	Instrumentation	Analytical Method	Reporting Limit	Detection Limit
Suspended Solid (SS)	Weighting	APHA 2540-D	0.5mg/L	0.5mg/L

- (g) Other relevant data were recorded, including monitoring location / position, time, water depth, tidal stages, weather conditions and any special phenomena or work underway at the construction site in the field log sheet for information.

4.5.3 Maintenance and Calibration

- (a) All in situ monitoring instruments would be calibrated and calibrated by ALS Technichem (HK) Pty Ltd. before use and at 3-monthly intervals throughout all stages of the water quality monitoring programme. Calibration details are provided in Appendix E.
- (b) The dissolved oxygen probe of YSI 6820 was calibrated by wet bulb method. Before the calibration routine, the sensor for dissolved oxygen was thermally equilibrated in water-saturated air. Calibration cup is served as a calibration chamber and it was loosened from airtight condition before it is used for the calibration. Calibration at ALS Technichem (HK) Pty Ltd. was carried out once every three months in a water sample with a known concentration of dissolved oxygen. The sensor was immersed in the water and after thermal equilibration, the known mg/L value was keyed in and the calibration was carried out automatically.
- (c) The turbidity probe of YSI 6820 is calibrated two times a month. A zero check in distilled water was performed with the turbidity probe of YSI 6820 once per monitoring day. The probe will be calibrated with a solution of known NTU at ALS Technichem (HK) Pty Ltd. once every three months.

4.6 Monitoring Schedule for the Reporting Month

- 4.6.1 The schedule for impact water quality monitoring in December 2015 is provided in Appendix F.
- 4.6.2 Results and Observations
- 4.6.3 Impact water quality monitoring results and graphical presentations are provided in Appendix J.

Table 4.5 Summary of Water Quality Exceedances

Station	Exceedance Level	DO (S&M)		DO (Bottom)		Turbidity		SS		Total	
		Ebb	Flood	Ebb	Flood	Ebb	Flood	Ebb	Flood	Ebb	Flood
IS5	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)6	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS7	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS8	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)9	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS10	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)11	Action	0	0	0	0	0	0	0	(1) 28 Dec 15	0	(1) 28 Dec 15
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)16	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS17	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR3	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR4(N)	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR5	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR6	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR7	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR10A	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR10B (N)	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
Total	Action	0	0	0	0	0	0	0	(1) 28 Dec 15	0	(1) 28 Dec 15
	Limit	0	0	0	0	0	0	0	0	0	0

Note: S: Surface; and
M: Mid-depth.

4.6.4 One action level impact water quality monitoring exceedance has been recorded in the reporting month.

4.6.4.1 Layout map below shows the construction activities conducted during flood tide on 28 December 2015, no marine work or barge was working at north of HKBCF reclamation works near the sea area or area where IS(Mf)11 is located, therefore the construction activities was considered unlikely to cause the SS exceedances recorded at IS(Mf)11 during mid-flood tide on 28 December 2015.

4.6.4.2 Exceedance recorded at IS(Mf)11 during mid-flood tide are unlikely due to marine based construction activities of the Project because:

4.6.4.3 With reference to the silt curtain checking record, defects such as disconnection of the silt curtain was not observed at north part of the perimeter silt curtain which are close to the IS(Mf)11.

4.6.4.4 Furthermore, no filling activities was observed in progress at the sea area north to HKBCF reclamation works and no silt plume was observed to flow from the inside of the perimeter silt curtain to the outside of the perimeter silt curtain when monitoring was conducted at IS(Mf)11. Also refer to the attached photo record taken at sea area located north of HKBCF reclamation works on 28 December 2015 for reference of sea condition on 28 December 2015, which shows that no silt plume was observed.

4.6.4.5 Photo record which shows the sea condition at southern part of the HKBCF reclamation works on 28 December 2015. No silt plume was observed.



4.6.4.6 The turbidity data obtained on 28 December 2015 from monitoring station IS10 and IS(Mf)11, SR7 and IS17 which located at/near the vicinity of sea area at north of HKBCF reclamation works, did not exceed the action and limit level. This indicates the turbidity level at/near IS(Mf)11 was not adversely affected.

4.6.4.7 As such, the exceedance was likely due to local effects in the vicinity of IS(Mf)11.

4.6.4.8 Action taken under the action plan:

1. Not applicable as SS was not measured *in situ*;
2. After considering the above mentioned investigation results, it appears that it was unlikely that the SS exceedances were attributed to active construction activities of this Contract;
3. IEC, contractor and ER were informed via email;
4. Monitoring data, all plant, equipment and Contractor's working methods were checked;
5. Since it is considered that the SS exceedance is unlikely to be project related, as such, actions 5-7 under the EAP are not considered applicable.

4.6.4.9 Nevertheless, the Contractor was reminded to ensure provision of ongoing maintenance to the silt curtains and to carry out maintenance work once defects were found.

4.6.4.10 Maintenance work of the silt curtain was carried out by the Contractor on a daily basis except Sunday and public holiday.

4.6.5 The event action plan is annexed in Appendix L.

5 DOLPHIN MONITORING

5.1 Monitoring Requirements

- 5.1.1 Vessel based surveys for the Chinese White Dolphin (CWD), *Sousa chinensis*, are to be conducted by a dedicated team comprising a qualified marine mammal ecologist and experienced marine mammal observers (MMOs). The purpose of the surveys are to evaluate the impact of the HKCBF reclamation and, if deemed detrimental, to take appropriate action as per the EM&A manual.
- 5.1.2 This 'Impact Monitoring' follows several months of 'Baseline Monitoring' so similar survey methodologies have been adopted to facilitate comparisons between datasets. Further, the data collected are compatible with, and are available for, incorporation into the data set managed by the Agriculture, Fisheries and Conservation Department (AFCD) as part of Hong Kong's long term Marine Mammal Monitoring Programme.

5.2 Monitoring Equipment

Table 5.1 summarises the equipment used for the impact dolphin monitoring.

Table 5.1 Dolphin Monitoring Equipment

Equipment	Model
Commercially licensed motor vessel	15m in length with a 4.5m viewing platform
Global Positioning System (GPS) x2	Integrated into T7000 Garmin GPS Map 76C
Computers (T7000 Tablet, Intel Atom)	Windows 7/MSO 13 Logger
Camera	Nikon D7100 300m 2.8D fixed focus Nikon D90 80-400mm zoom lens
Laser Rangefinder	Range Finder Bushnell 1000m
Marine Binocular x3	Nexus 7 x 50 marine binocular with compass and reticules Fujinon 7 x 50 marine binocular with compass and reticules

5.3 Monitoring Frequency and Conditions

- 5.3.1 Dolphin monitoring is conducted twice per month in each survey area.
- 5.3.2 Dolphin monitoring is conducted only when visibility is good (e.g., over 1km) and the sea condition is at a Beaufort Sea State of 4 or better.
- 5.3.3 When thunder storm, black rain or typhoon warnings are in force, all survey effort is stopped.

5.4 Monitoring Methodology and Location

- 5.4.1 The impact dolphin monitoring is vessel-based and combines line-transect and photo-ID methodology. The survey follows pre-set and fixed transect lines in the two areas defined by AFCD as:
- 5.4.2 Northeast Lantau survey area; and
- 5.4.3 Northwest Lantau survey area.
- 5.4.4 The co-ordinates for the transect lines and layout map have been provided by AFCD and are shown in Table 5.2 and Figure 4.

Table 5.2 Impact Dolphin Monitoring Line Transect Co-ordinates (Provided by AFCD)

ID	HK Grid System		Long Lat in WGS84	
	X	Y	Long	Lat
1	804671	815456	113.870287	22.277678
1	804671	831404	113.869975	22.421696
2	805475	815913	113.878079	22.281820
2	805477	826654	113.877896	22.378814
3	806464	819435	113.887615	22.313643
3	806464	822911	113.887550	22.345030
4	807518	819771	113.897833	22.316697
4	807518	829230	113.897663	22.402113
5	808504	820220	113.907397	22.320761
5	808504	828602	113.907252	22.396462
6	809490	820466	113.916965	22.323003
6	809490	825352	113.916884	22.367128
7	810499	820880	113.926749	22.326757
7	810499	824613	113.926688	22.360464
8	811508	821123	113.936539	22.328966
8	811508	824254	113.936486	22.357241
9	812516	821303	113.946320	22.330606
9	812516	824254	113.946279	22.357255
10*	813525	820827	113.956112	22.326321
10*	813525	824657	113.956066	22.360908
11	814556	818853	113.966155	22.304858
11	814556	820992	113.966125	22.327820
12	815542	818807	113.975726	22.308109
12	815542	824882	113.975647	22.362962
13	816506	819480	113.985072	22.314192
13	816506	824859	113.985005	22.362771
14	817537	820220	113.995070	22.320883
14	817537	824613	113.995018	22.360556
15	818568	820735	114.005071	22.325550
15	818568	824433	114.005030	22.358947
16	819532	821420	114.014420	22.331747
16	819532	824209	114.014390	22.356933
17	820451	822125	114.023333	22.338117
17	820451	823671	114.023317	22.352084
18	821504	822371	114.033556	22.340353
18	821504	823761	114.033544	22.352903
19	822513	823268	114.043340	22.348458
19	822513	824321	114.043331	22.357971
20	823477	823402	114.052695	22.349680
20	823477	824613	114.052686	22.360610
21	805476	827081	113.877878	22.382668
21	805476	830562	113.877811	22.414103
22	806464	824033	113.887520	22.355164
22	806464	829598	113.887416	22.405423
23	814559	821739	113.966142	22.334574
23	814559	824768	113.966101	22.361920

Remarks:

(a) *Due to the presence of deployed silt curtain systems at the site boundaries of the Project, some of the transect lines shown in Figure 5 could not be fully surveyed during the regular survey. Transect 10 is reduced from 6.4km to approximately 3.6km in length due to the HKBCF construction site. Therefore the total transect length for both NEL and NWL combined is reduced to approximately 108km.

(b) Coordinates for transect lines 1, 2, 7, 8, 9 and 11 have been updated in respect to the Proposal for Alteration of Transect Line for Dolphin Monitoring approved by EPD on 19 August 2015.

5.5 Monitoring Procedures

- 5.5.1 The study area incorporates 23 transects which are to be surveyed twice per month. Each survey day lasts approximately 9 hours.
- 5.5.2 The survey vessel departs from Tung Chung Development Pier, Tsing Yi Public Pier or the nearest safe and convenient pier.
- 5.5.3 When the vessel reaches the start of a transect line, “on effort” survey begins. Areas between transect lines and traveling to and from the study area are defined as “off effort”.
- 5.5.4 The transect line is surveyed at a speed of 6-8 knots (11-14 km/hr). For the sake of safety, the speed was sometimes a bit slower to avoid collision with other vessels. During some periods, tide and current flow in the survey areas exceeds 7 knots which can affect survey speed. There are a minimum of four marine mammal observers (MMOs) present on each survey, rotating through four positions, observers (2), data recorder (1) and ‘rest’ (1). Rotations occur every 30 minutes or at the end of dolphin encounters. The data recorder records effort, weather and sightings data directly onto the programme Logger and is not part of the observer team. The observers search with naked eye and binoculars between 90° and 270° abeam (bow being 0°).
- 5.5.5 When a group of dolphins is sighted, position, bearing and distance data are recorded immediately onto the computer and, after a short observation, an estimate made of group size. These parameters are linked to the time-GPS-ships data which are automatically stored in the programme Logger throughout the survey period. In this manner, information on heading, position, speed, weather, effort and sightings are stored in a format suitable for use with DISTANCE software for subsequent line transect analyses.
- 5.5.6 Once the vessel leaves the transect line, it is deemed to be “off effort”. The dolphins are approached with the purpose of taking high resolution pictures for proper photo-identification of individual CWD. Attempts to photograph all dolphins in the group are made. Both the left and right hand sides of the dorsal fin area of each dolphin in the group are photographed, if possible. On finishing photographing, the vessel will return to the transect line at the point of departure and “on effort” survey is resumed.
- 5.5.7 Sightings which are made while on the transect line are referred to as “on effort sightings”, while not on the actual transect line are referred to as an “opportunistic sightings” (e.g. another group of dolphins is sighted while travelling back to the transect line). Only “on effort sightings” can be used in analyses which require effort or rate quantification, e.g., encounter rate per 100km searched. This is also how “on effort sightings” are treated in the baseline report. “Opportunistic sightings” provide additional information on individual habitat use and population distribution and they are noted accordingly.
- 5.5.8 As time and GPS data are automatically logged throughout the survey and are linked to sightings data input, start and end times of encounters and deviation from the transect lines are recorded and can be subsequently reviewed.

5.6 Monitoring Schedule for the Reporting Month

- 5.6.1 The schedule for dolphin monitoring in December 2015 is provided in Appendix F.
- 5.6.2 Two surveys covering both study areas were completed.

5.7 Results and Observations

- 5.7.1 Dolphin surveys were conducted on 1, 2, 7 and 8 December 2015. A total of 217.5 km of transect line was conducted, all 217.5km was conducted during Beaufort Sea State 3 or better (favourable water conditions).

The effort summary and sightings data are shown in Tables 5.3 and 5.4, respectively. The survey efforts conducted in December 2015 are plotted in Figure 5a-b. For Table 5.3, only on-effort information is included. Transects conducted in all Beaufort Sea State are included. Compared to previous monthly reports, the whole number Beaufort Sea State scale is used so as to ease comparison with other dolphin monitoring reports.

Table 5.3 Impact Dolphin Monitoring Survey Effort Summary, Effort by Area and Beaufort Sea State

Survey	Date	Area	Beaufort	Effort (km)	Total Distance Travelled (km)
1	12/01/2015	NWL	1	27.6	109.0
	12/01/2015	NWL	2	27.8	
	12/01/2015	NWL	3	10.9	
	12/02/2015	NWL	1	3.4	
	12/02/2015	NWL	2	2.8	
	12/02/2015	NEL	1	31.6	
	12/02/2015	NEL	2	4.9	
2	12/07/2015	NWL	1	3.1	108.5
	12/07/2015	NWL	2	9.2	
	12/07/2015	NWL	3	10.7	
	12/07/2015	NEL	1	26.8	
	12/07/2015	NEL	2	9.8	
	12/08/2015	NWL	1	0.3	
	12/08/2015	NWL	2	40.3	
	12/08/2015	NWL	3	8.3	
TOTAL in December 2015					217.5

*Remark: Surveys conduct under Beaufort Sea State 3 or below are considered as under favourable condition.

Table 5.4 Impact Dolphin Monitoring Survey Details December 2015

Date	Location	No. Sightings "on effort"	No. Sightings "opportunistic"
01/12/2015	NWL	2	0
	NEL	0	0
02/12/2015	NWL	0	0
	NEL	0	0
07/12/2015	NWL	0	0
	NEL	0	0
08/12/2015	NWL	0	0
	NEL	0	0
TOTAL in December 2015		2	0

*Location indicates which area was being surveyed when the sighting was made. The area noted does not necessarily indicate where the dolphins were when the sighting was made.

Table 5.5 The Encounter Rate of Number of Dolphin Sightings & Total Number of Dolphins per Area[^]

Encounter Rate of Number of Dolphin Sightings (STG)*						
Date	NEL Track (km)	NWL Track (km)	NEL Sightings	NWL Sightings	NEL Encounter Rate	NWL Encounter Rate
1 & 2 Dec 15	36.5	72.5	0	2	0.0	2.8
7 & 8 Dec 15	36.6	71.9	0	0	0.0	0.0
Encounter Rate of Total Number of Dolphins (ANI)**						
Date	NEL Track (km)	NWL Track (km)	NEL Dolphins	NWL Dolphins	NEL Encounter Rate	NWL Encounter Rate
1 & 2 Dec 15	36.5	72.5	0	11	0.0	15.2
7 & 8 Dec 15	36.6	71.9	0	0	0.0	0.0

* Encounter Rate of Number of Dolphin Sightings (STG) presents encounter rates in terms of groups per 100km.

** Encounter Rate of Total Number of Dolphins (ANI) presents encounter rates in terms of individuals per 100km. And the encounter rate is not corrected for individuals, calculation may represent double counting.

[^]The table is made only for reference to the quarterly STG & ANI, which were adopted for the Event & Action Plan.

- 5.7.2 A total of two sightings were made, both are “on effort” sighting and were recorded on the 1 December 2015. Details are summarised and plotted in Appendix K and Figure 5c, respectively. The first group sighted on 1 December 2015 contained 3 individuals, second group contained 8 individuals.
- 5.7.3 No calf was observed in December 2015
- 5.7.4 Behaviour: On the 1 December 2015, the first group was travelling and the second group was engaged in multiple behaviours, i.e., feeding and active surfacing.
- 5.7.5 One resighting of HZMB 114 was recorded in November 2015. This individual has been sighted once previously, in October 2013, in NWL. Images and re-sightings data are included in Appendix K.
- 5.7.6 Noteworthy Observation¹:
 - 5.7.6.1 When impact monitoring was conducted at the southern parts of transect lines 1 & 2, the view of the area was partially blocked by the working vessels and fixed structures which do not belong to HKBCF Reclamation Works. The number of fixed structures has increased and in many areas, it is no longer possible to pass between them by ship. As the working vessels will move during the on-going works, it is considered that they will temporarily affect survey protocol, survey data collection, dolphin movement, dolphin habitat use and dolphin behaviour, whereas the fixed structures will continuously affect survey protocol, survey data collection, dolphin movement, dolphin habitat use and dolphin behaviour.
 - 5.7.6.2 The HKBCF and adjoining “Southern Landfall” Projects effected lines 10, 11, 12, 13 and 23. The view of the area was partially blocked by the working vessels and in water structures. As the working vessels will move as construction progresses, they will cause temporary effects to survey protocol and survey data collection. In time, the fixed structures will affect all survey protocols and dolphin ecology in the long term. As construction is ongoing, it is not yet known if these fixed structures will affect the transect lines passage.
 - 5.7.6.3 Travel to the northern end of line 10 and 18 was slightly impeded by the anchorage located there. After checking with the Contractor, there are no trans-boundary vessels that are required to anchor at northern ends of lines 10 and 18 during this reporting period, as such they are unlikely to be related to

¹ A noteworthy observation is to show that either the conduct of the surveys themselves is affected, i.e., the noted vessel or works impedes the progress or view of the survey platform. In addition, the vessel or construction works may be different or additional to that observed previously and further, are of such a nature that they are a likely to create an impact on the movement or behaviour of the subject of the impact survey, in this case, the dolphins.

this Contract. As there are variable numbers of ships in this anchorage through time, it is considered that this could temporarily affect survey protocol, survey data collection and dolphin habitat use.

- 5.7.6.4 Anchored fishing vessels were noted on lines 1 and 2. In previous encounters, dolphins were seen feeding in association with these vessels despite them not being active. This may influence both dolphin behaviour and the view of the area.
- 5.7.6.5 Anchored vessels were noted on line 18 which caused our vessel to divert slightly from the trackline. It is unknown who these vessels belong to or even if they were Project related.
- 5.7.6.6 New projects were ongoing at the southern end of line 5 which were not part of this Project. There are no apparent fixed structures associated with these projects only platforms and servicing vessels. As it is not known what activity was being conducted, the effect that these projects may have specifically on dolphins is not known. There is no signage on this new project and it is not part of HKBCF Reclamation Works.
- 5.7.6.7 The survey effort log notes the areas in which the visibility is limited or the survey is affected so that these can be accounted for in any subsequent analyses. Some of these obstructions will become permanent and some will be temporary as the HZMB is built and other projects progress. It is advised that the impact monitoring surveys should be completed as close to the predefined lines as possible (as per Figure 4 of this report).
- 5.7.6.8 The above noteworthy observations are largely a result of multiple and on-going infrastructure projects within the Lantau area. No amendment to EM&A protocols can negate the effects of these projects, e.g., it is a highly dynamic environment and viewing conditions may alter every survey (sometimes within surveys) and most of the survey area is affected, to some degree, by marine construction works. Instead, survey data analyses should incorporate any noteworthy observations which may affect either data collection or dolphin distribution and behavioural changes. The above mentioned activities recorded during boat survey will not affect implementation of the EM&A Programme provided appropriate data analyses are conducted.
- 5.7.7 The event action plan is annexed in Appendix L.

6 ENVIRONMENTAL SITE INSPECTION AND AUDIT

6.1 Site Inspection

6.1.1 Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. In the reporting month, 5 site inspections were carried out on 3, 10, 17, 23 and 31 December 2015.

6.1.2 Particular observations during the site inspections are described below:

Air Quality

6.1.3 Dark smoke was observed at portion C2a when a vessel was in operation. The Contractor was reminded to prevent. (Reminder)

6.1.4 Two idling generators were found at Portion B without proper NRMM labels. The Contractor was reminded to label the generator properly. Subsequently, the Contractor properly labelled one of the generator and the Contractor was reminded to label the another generator properly. As informed by the Contractor, another idle generator was provided with NRMM label and removed from site. (Closed)

Noise

6.1.5 No relevant adverse impact was observed in the reporting month.

Water Quality

- 6.1.6 Insufficient sand bund was observed at Portion C2b when DCM was conducted. The Contractor was reminded to provide sufficient bunding to prevent potential runoff. The Contractor subsequently enhanced sand bund at the works area. (Closed)

Chemical and Waste Management

- 6.1.7 Chemical container was observed placing on bare ground at Portion C2b. The Contractor should provide drip trays as proper chemical container storage measure. Subsequently, the Contractor provided drip tray to oil drums. (Closed)
- 6.1.8 General refuse was observed on site, on ground at Portion D and on ground at portion C2a, the Contractor was reminded to clear the general refuse and keep the site clean and tidy. Subsequently, the Contractor collected and cleared the general refuse and kept the site clean and tidy. (Closed)
- 6.1.9 Oil drums was observed without drip tray at Portion C2b, the Contractor was reminded to provided drip tray to oil drums. The Contractor subsequently removed the oil drums from the concerned area. (Closed)
- 6.1.10 Oil water mixture was observed accumulated inside bunding. The Contractor was reminded to regularly clear the oil water mixture accumulated inside drip tray. Subsequently, the Contractor removed the oil water mixture accumulated inside drip tray. (Closed)

Landscape and Visual Impact

- 6.1.11 No relevant adverse impact was observed in the reporting month.

Others

- 6.1.12 No relevant adverse impact was observed in the reporting month.

6.2 Advice on the Solid and Liquid Waste Management Status

- 6.2.1 The Contractor had registered as a chemical waste producer for this Project. Receptacles were available for general refuse collection and sorting.
- 6.2.2 As advised by the Contractor, 23,040m³ of fill were imported for the Project use in the reporting period. 84.5m³ of general refuse were generated and disposed of in the reporting period. Monthly summary of waste flow table is detailed in Appendix M.
- 6.2.3 The Contractor is advised to properly maintain on site C&D materials and wastes storage, collection, sorting and recording system, dispose of C&D materials and wastes at designated ground and maximize reuse / recycle of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.
- 6.2.4 The Contractor is reminded that chemical waste should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labeling and Storage of Chemical Wastes.
- 6.2.5 The treated marine sediment and/or excavated filling material specified by Contract no. HY/2013/01 was received as public fill for Contract no. HY/2010/02's reclamation filling works since January 2015. Such site arrangement was on-going in the reporting month and will be regularly reviewed and reported in the coming monthly EM&A report.

6.3 Environmental Licenses and Permits


6.3.1 The environmental licenses and permits for the Project and valid in the reporting month is summarized in Table 6.1.

Table 6.1 Summary of Environmental Licensing and Permit Status

Statutory Reference	License/ Permit	License or Permit No.	Valid Period		License/ Permit Holder	Remarks
			From	To		
EIAO	Environmental Permit	EP-353/2009/I	17/07/2015	N/A	HyD	Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities
		EP-354/2009/D	13/03/2015	N/A		Tuen Mun – Chek Lap Kok Link (TMCLKL Southern Landfall Reclamation only)
APCO	NA notification	--	30/12/2011	--	CHEC	Works Area WA2 and WA3
APCO	NA notification	--	25/07/2014	--	CHEC	Works Area WA1
WDO	Chemical Waste Producer Registration	5213-951-C1186-30	28/10/2015	N/A	CHEC	Chemical waste produced in Contract HY/2010/02 (WA1)
WDO	Chemical Waste Producer Registration	5213-951-C1186-21	30/3/2012	N/A	CHEC	Chemical waste produced in Contract HY/2010/02 (WA2)
WDO	Chemical Waste Producer Registration	5213-839-C3750-02	13/09/2012	--	CHEC	Registration as Chemical Waste Producer at TKO 137(FB)
WDO	Billing Account for Disposal of Construction Waste	7014181	05/12/2011	N/A	CHEC	Waste disposal in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RS0536-15	06/06/2015	05/12/2015	CHEC	Reclamation Works in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RS1240-15	18/11/2015	28/02/2016	CHEC	Reclamation Works in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RE1214-15	20/12/2015	19/06/2016	CHEC	Section of TKO Fill Bank under Contract HY/2010/02

6.4 Implementation Status of Environmental Mitigation Measures

- 6.4.1 In response to the site audit findings, the Contractors carried out corrective actions.
- 6.4.2 A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in Appendix C. Most of the necessary mitigation measures were implemented properly.
- 6.4.3 Training of marine travel route for marine vessels operator was given to relevant staff and relevant records were kept properly.
- 6.4.4 Regarding the implementation of dolphin monitoring and protection measures (i.e. implementation of Dolphin Watching Plan, Dolphin Exclusion Zone and Silt Curtain integrity Check), regular checking were conducted by the experienced MMOs within the works area to ensure no dolphin was trapped by the enclosed silt curtain systems. Any dolphin spotted within the enclosed silt curtain systems was reported and recorded. Relevant procedures were followed and measures were well implemented. Silt curtain systems were also inspected timely in accordance to the submitted plan. All inspection records were kept properly.
- 6.4.5 Acoustic decoupling measures on noisy plants on construction vessels were checked regularly and the Contractor was reminded to ensure provision of ongoing maintenance to noisy plants and to carry out improvement work once insufficient acoustic decoupling measures were found.
- 6.4.6 Frequency of watering per day on exposed soil was checked; with reference to the record provided by the Contract, watering was conducted at least 8 times per day on reclaimed land. The frequency of watering is the mainly refer to water truck. Sprinklers are only served to strengthen dust control measure for busy traffic at the entrance of Portion D. As informed by the Contractor, during the malfunction period of sprinkler, water truck will enhance watering at such area. The Contractor was reminded to ensure provision of watering of at least 8 times per day on all exposed soil within the Project site and associated works areas throughout the construction phase.
- 6.4.7 As informed by the Contractor on 23 December 2015, an oil spillage incident was observed near Cell No. 28 on 23 December 2015. For the location of the oil spillage recorded on 23 December 2015, also refer to the map shown below.

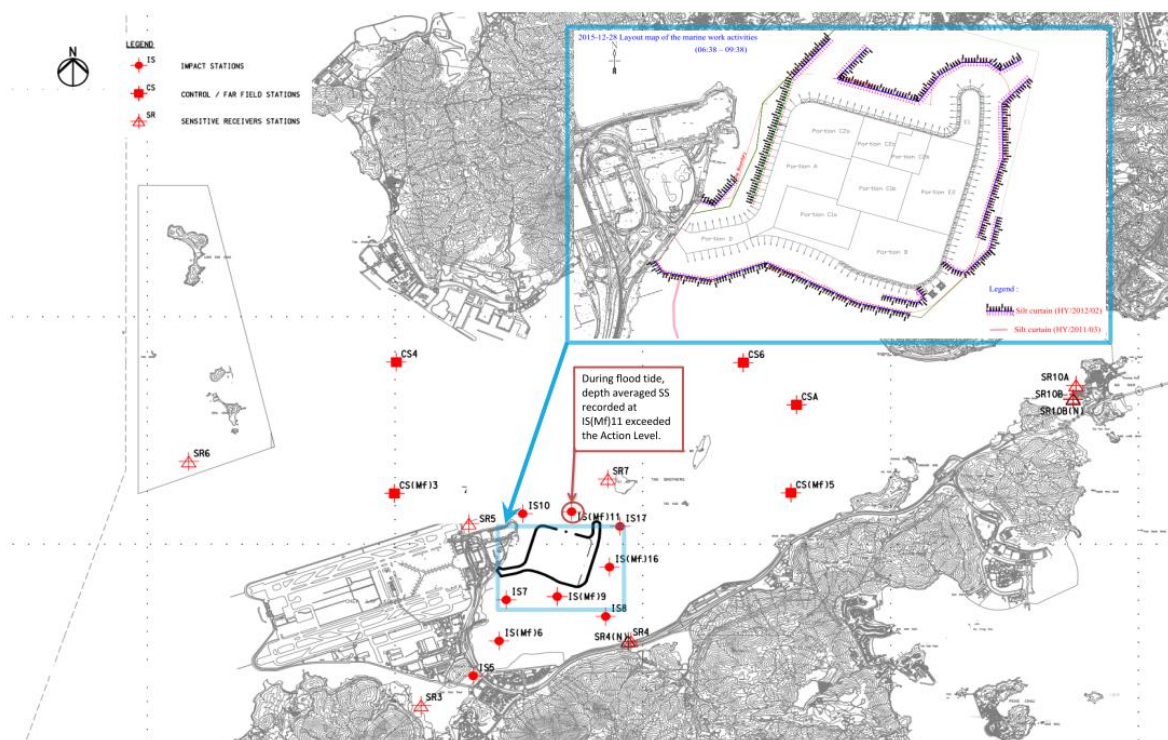

6.4.7.1 Details of the oil spillage incident (23 December 2015) including size, location, time of the spillage and Contractor's actions taken in response to the spill incident have been reviewed and summarised as follow:

- Oil on sea was observed on sea area near Cell No. 28 within perimeter silt curtain at 09:30 a.m. on 23 December 2015 by the Contractor and RSS (also refer to attached layout map).
- The Contractor organised manpower to identify the spill source, but the source of oil spill was not identified.
- The Contractor equipped people involved in the cleanup works with personal protective equipment such as gloves prior to the removal of any leaked chemical or chemical waste.
- Pads and Pillow of the Spill Kit were applied to absorb and remove the spillage.

6.4.7.2 Impact water quality monitoring records of 23 December 2015 have been reviewed.

6.4.7.3 Observations and Results:

- Oil on sea was observed on sea area near Cell No. 28 within perimeter silt curtain at 09:30 a.m. on 23 December 2015 by the Contractor and RSS (also refer to above layout map).
- The following photo record shows the sea condition when the oil spillage on sea was observed.



6.4.7.4 The following actions were taken by the Contractor:

- The Contractor organized manpower to identify the spill source. During inspection, no construction vessel was observed around the concerned area and the source of oil spill was not identified.
- The oil spill was identified during inspection conducted by the Contractor and RSS on 23 December 2015 as discrete, non-continuous source with approximately 50m² spread. The below photo shows that the Contractor deployed absorption booms to remove the floating oil from water.



- 6.4.7.5 The below photos shows that the used absorption booms were collected using disposal bags as part of the spill kits item. The used absorption booms were disposed of as chemical waste by the Contractor.



- 6.4.7.6 The oil stain observed was limited at nearby southern sea area within the silt curtain.
- 6.4.7.7 No more sign of oil spillage was found on the nearby water after the clean-up.
- 6.4.7.8 Review of impact water quality monitoring data of 23 December 2015:
- 6.4.7.9 Monitoring stations IS7, IS(Mf)9, IS8, IS(Mf)6 and SR4(N) are the monitoring stations close to location of observed oil spill (also refer to above layout map). Impact water quality monitoring data recorded at monitoring station, IS7, IS(Mf)9, IS8, IS(Mf)6 and SR4 on 23 December 2015 were reviewed. There was no water quality exceedance recorded at IS7, IS(Mf)9, IS8, IS(Mf)6 and SR4(N) on 23 December 2015. Please also see attached for detail of water quality monitoring data obtained on 23 December 2015.
- 6.4.7.10 The Contractor was reminded to continue to follow the spill response plan when oil is observed on sea.

6.5 Summary of Exceedances of the Environmental Quality Performance Limit

- 6.5.1 For impact air quality monitoring, no exceedance of 1-Hour TSP or 24-Hour TSP was recorded at all monitoring stations in the reporting month.
- 6.5.2 For construction noise, no exceedance was recorded at all monitoring stations in the reporting month.
- 6.5.3 One (1) action level impact water quality monitoring exceedance at monitoring station IS(Mf)11 has been recorded on 28 December 2015 during flood tide. After investigation, there is no adequate information to conclude the recorded exceedance is related to this Contract.
- 6.5.4 For Dolphin monitoring, a total of two sightings were made, both are “on effort” sighting and were recorded on 1 December 2015. Details are summarised and plotted in Appendix K and Figure 5c, respectively. The first group sighted on 1 December 2015 contained 3 individuals, second group contained 8 individuals. No calf was observed in December 2015.
- 6.5.5 Dolphin behaviour: On 1 December 2015, the first group was travelling and the second group was engaged in multiple behaviours, i.e., feeding and active surfacing.
- 6.5.6 Environmental site inspection was carried out 5 times in December 2015. Recommendations on remedial actions were given to the Contractors for the deficiencies identified during the site audits.
- 6.5.7 Cumulative statistics on exceedance is provided in Appendix N.

6.6 Summary of Complaints, Notification of Summons and Successful Prosecutions

- 6.6.1 The Environmental Complaint Handling Procedure is annexed in Figure 6.
- 6.6.2 A water quality complaint was referred to the ENPO at 10:22 am on the 4 December 2015 by EPD; ENPO referred this complaint to this Contract on the same day. With referred to the information provided by ENPO, EPD has contacted the complainant, and obtained the additional information from the complainant and it is suspected that the incident happened in the afternoon on 28 November 2015.
- 6.6.2.1 A video was provided by the complainant, the following photo is captured from the video which shows that turbid water was seen behind a barge, the incident is suspected to be happened in the afternoon on 28 November 2015.



6.6.2.2 Investigation actions:

- Review of the information (video and photo) provided by the complainant
- Checking whether there barge which is required to work at the concerned area for Contract HY/2010/02 HKBCF Reclamation Works in the afternoon on 28 November 2015

6.6.2.3 Investigation results:

- By tracing the turbid water showed on the attached photo, the source of turbid seawater is not from the inside or the near the site boundary Contract HY/2010/02 HKBCF Reclamation Works.

- In addition, after checking with the Contractor, there are no derrick/flat top barges travelled to or from the sea area adjacent to the north of Tung Chung Waterfront Road in the afternoon of 28 Nov 2015, as such, it is considered not related to this Contract.
- 6.6.2.4 Nevertheless, the Contractor was reminded to continue to fully maintain all water quality mitigation measures.
- 6.6.3 No notification of summons or prosecution was received in the reporting period.
- 6.6.4 Statistics on complaints, notifications of summons and successful prosecutions are summarized in Appendix N.

6 FUTURE KEY ISSUES

7.1 Construction Programme for the Coming Months

7.1.1 As informed by the Contractor, the major works for the Project in January 2016 and February 2016 will be *:-

Marine-base

- Rock fill
- Conforming Sloping Seawalls
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Rubble Mound Seawall

Land-base

- Surcharge removal & laying
- Deep Cement Mixing
- Removal of Temporary Seawall
- Vertical Band Drains
- Installations of Precast Culverts except sloping outfalls
- Geotechnical Instrumentation Works
- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Maintenance of Temporary Marine Access at Works Area WA2

*Construction activities in January 2016 and February 2016 will be changed subject to works progress.

7.2 Key Issues for the Coming Month

7.2.1 Key issues to be considered in the coming months:-

- Site runoff should be properly collected and treated prior to discharge;
- Minimize loss of sediment from filling works;
- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities;
- Exposed surfaces/soil stockpiles should be properly treated to avoid generation of silty surface runoff during rainstorm;
- Regular review and maintenance of wheel washing facilities provided at all site entrances/exits;
- Conduct regular inspection of various working machineries and vessels within works areas to avoid any dark smoke emission;
- Suppress dust generated from work processes with use of bagged cements, earth movements, excavation activities, exposed surfaces/soil stockpiles and haul road traffic;
- Quieter powered mechanical equipment should be used;
- Provision of proper and effective noise control measures for operating equipment and machinery on-site, such as erection of movable noise barriers or enclosure for noisy plants;
- Closely check and replace the sound insulation materials regularly;
- Better scheduling of construction works to minimize noise nuisance;
- Properly store and label oil drums and chemical containers placed on site;
- Proper chemicals, chemical wastes and wastes management;
- Maintenance works should be carried out within roofed, paved and confined areas;
- Collection and segregation of construction waste and general refuse on land and in the sea should be carried out properly and regularly; and
- Proper protection and regular inspection of existing trees, transplanted/retained trees.
- Control night-time lighting and glare by hooding all lights.
- Regular review and provide maintenance to dust control measures such as sprinkler system.

7.3 Monitoring Schedule for the Coming Month

- 7.3.1 The tentative schedule for environmental monitoring in January 2016 is provided in Appendix F.

8 CONCLUSIONS AND RECOMMENDATIONS

8.1 Conclusions

- 8.1.1 The construction phase and EM&A programme of the Project commenced on 12 March 2012.
- 8.1.2 For construction noise, no exceedance was recorded at all monitoring stations in the reporting month.
- 8.1.3 For construction noise, no exceedance was recorded at all monitoring stations in the reporting month.
- 8.1.4 One (1) action level impact water quality monitoring exceedance at monitoring station IS(Mf)11 has been recorded on 28 December 2015 during flood tide. After investigation, there is no adequate information to conclude the recorded exceedance is related to this Contract.
- 8.1.5 For Dolphin monitoring, a total of two sightings were made, both are “on effort” sighting and were recorded on 1 December 2015. Details are summarised and plotted in Appendix K and Figure 5c, respectively. The first group sighted on 1 December 2015 contained 3 individuals, second group contained 8 individuals. No calf was observed in December 2015
- 8.1.6 Dolphin behaviour: On 1 December 2015, the first group was travelling and the second group was engaged in multiple behaviours, i.e., feeding and active surfacing.
- 8.1.7 A water quality complaint was referred to the ENPO at 10:22 am on the 4 December 2015 by EPD; ENPO referred this complaint to this Contract on the same day. With referred to the information provided by ENPO, EPD has contacted the complainant, and obtained the additional information from the complainant and it is suspected that the incident happened in the afternoon on 28 November 2015. A video was provided by the complainant who shows that turbid water behind a barge, the incident is suspected to be happened in the afternoon on 28 November 2015. After investigation, it is considered not related to this Contract.
- 8.1.8 No notification of summons or prosecution was received in the reporting period.
- 8.1.9 As informed by the Contractor on 23 December 2015, an oil spillage incident was observed near Cell No. 28 of HKBCF Reclamation Works on 23 December 2015. Spillage response actions were taken by the Contractor and no more sign of oil spillage was found on the nearby water after the clean-up. For details of investigation actions and results, please refer to section 6.4.7.
- 8.1.10 Environmental site inspection was carried out 5 times in December 2015. Recommendations on remedial actions were given to the Contractors for the deficiencies identified during the site audits.

8.2 Recommendations

8.2.1 According to the environmental site inspections performed in the reporting month, the following recommendations were provided:

Air Quality Impact

- All working plants and vessels on site should be regularly inspected and properly maintained to avoid dark smoke emission.
- All vehicles should be washed to remove any dusty materials before leaving the site.
- Haul roads should be sufficiently dampened to minimize fugitive dust generation.
- Wheel washing facilities should be properly maintained and reviewed to ensure properly functioning.
- Temporary exposed slopes and open stockpiles should be properly covered.
- Enclosure should be erected for cement debagging, batching and mixing operations.
- Water spraying should be provided to suppress fugitive dust for any dusty construction activity.
- Regular review and provide maintenance to dust control measures such as sprinkler system.

Construction Noise Impact

- Quieter powered mechanical equipment should be used as far as possible.
- Noisy operations should be oriented to a direction away from sensitive receivers as far as possible.
- Proper and effective noise control measures for operating equipment and machinery on-site should be provided, such as erection of movable noise barriers, enclosure for noisy plants or enhancement works to provide sufficient acoustic decoupling measure(s). Closely check and replace the sound insulation materials regularly
- Vessels and equipment operating should be checked regularly and properly maintained.
- Noise Emission Label (NEL) shall be affixed to the air compressor and hand-held breaker operating within works area.
- Acoustic decoupling measures should be properly implemented for all existing and incoming construction vessels with continuous and regularly checking to ensure effective implementation of acoustic decoupling measures.

Water Quality Impact

- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities in order to make sure they are functioning effectively.
- Construction of seawall should be completed as early as possible.
- Regular inspect and review the loading process from barges to avoid splashing of material.
- Silt, debris and leaves accumulated at public drains, wheel washing bays and perimeter u-channels and desilting facilities should be cleaned up regularly.
- Silty effluent should be treated/ desilted before discharged. Untreated effluent should be prevented from entering public drain channel.
- Proper drainage channels/bunds should be provided at the site boundaries to collect/intercept the surface run-off from works areas.
- Exposed slopes and stockpiles should be covered up properly during rainstorm.


Chemical and Waste Management

- All types of wastes, both on land and floating in the sea, should be collected and sorted properly and disposed of timely and properly. They should be properly stored in designated areas within works areas temporarily.
- All chemical containers, batteries and oil drums should be properly stored and labelled.
- All plants and vehicles on site should be properly maintained to prevent oil leakage. Proper measures, like drip trays and/or bundings, should be provided for retaining leaked oil/chemical from plants.
- All kinds of maintenance works should be carried out within roofed, paved and confined areas.
- All drain holes of the drip trays utilized within works areas should be properly plugged to avoid any oil and chemical waste leakage.
- Oil stains on soil surface, accumulated oil mixture and empty chemical containers should be cleared and disposed of as chemical waste.
- Regular review should be conducted for working barges and patrol boats to ensure sufficient measures and spill control kits were provided on working barges and patrol boats to avoid any spreading of leaked oil/chemicals.

Landscape and Visual Impact

- All existing, retained/transplanted trees at the works areas should be properly fenced off and regularly inspected.
- Control night-time lighting and glare by hooding all lights.

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON-SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

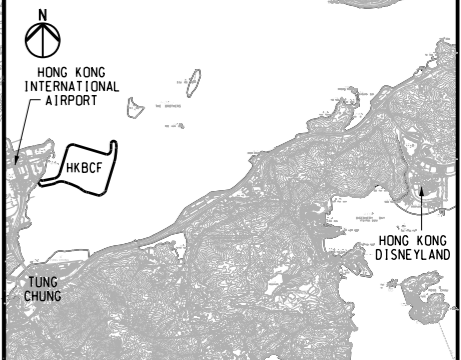

KEY PLAN

- NOTES**
1. ALL COORDINATES ARE RELATED TO HONG KONG 1980 GRID.
 2. ALL LEVELS ARE IN METRES ABOVE HONG KONG PRINCIPAL DATUM (mPD).
 3. REFER TO DRG NO. 211036/SL/1002 FOR THE DEFINITION OF SETTING OUT LINE (SOL) FOR THE HONG KONG BOUNDARY CROSSING FACILITIES (HKBCF) RECLAMATION SITE.
 4. REFER TO DRG NO. 211036/SL/1004 FOR DETAILS OF SITE BOUNDARY.
 5. FOR EXTENT OF SORTING FACILITIES AT FILL BANK AT TSEUNG KWAN O AREA 137 REFER TO DRG NO. 211036/SL/1015.

- LEGEND**
- - - - - SITE BOUNDARY
 - - - - - SETTING OUT LINE (SOL)
 - - - - - WORKS AREA BOUNDARY

Rev	Description	By	Date
-	FOR CONSTRUCTION	HYJL	11/11

Consultant

ARUP 奧雅納工程顧問
Ove Arup & Partners Hong Kong Limited

Supported By :

- Ecosystems Ltd.
- EDA Marine Ltd.
- Geotechnical Consulting Group (Asia) Ltd.
- Hong Kong Cetacean Research Project
- IntelBuild Technyx Asia Limited
- Tony Gee and Partners LLP


Contract No. and Title:
Contract No. HY/2010/02
Hong Kong-Zhuhai-Macao Bridge
Hong Kong Boundary Crossing Facilities
- Reclamation Works

Drawing title
KEY PLAN



Drawing no.	211036/SL/1001	Rev.	-
Drawn	RL	Date	11/09
Checked	KKY	Approved	DML
Scale	1:20000 @A1 1:40000 @A3	Status	WORKING



Printed by : 12/17/2011
Filename : J:\211036\RECORD\WORKING\20111130_Contract Drawing_211036_SL_1001.dgn

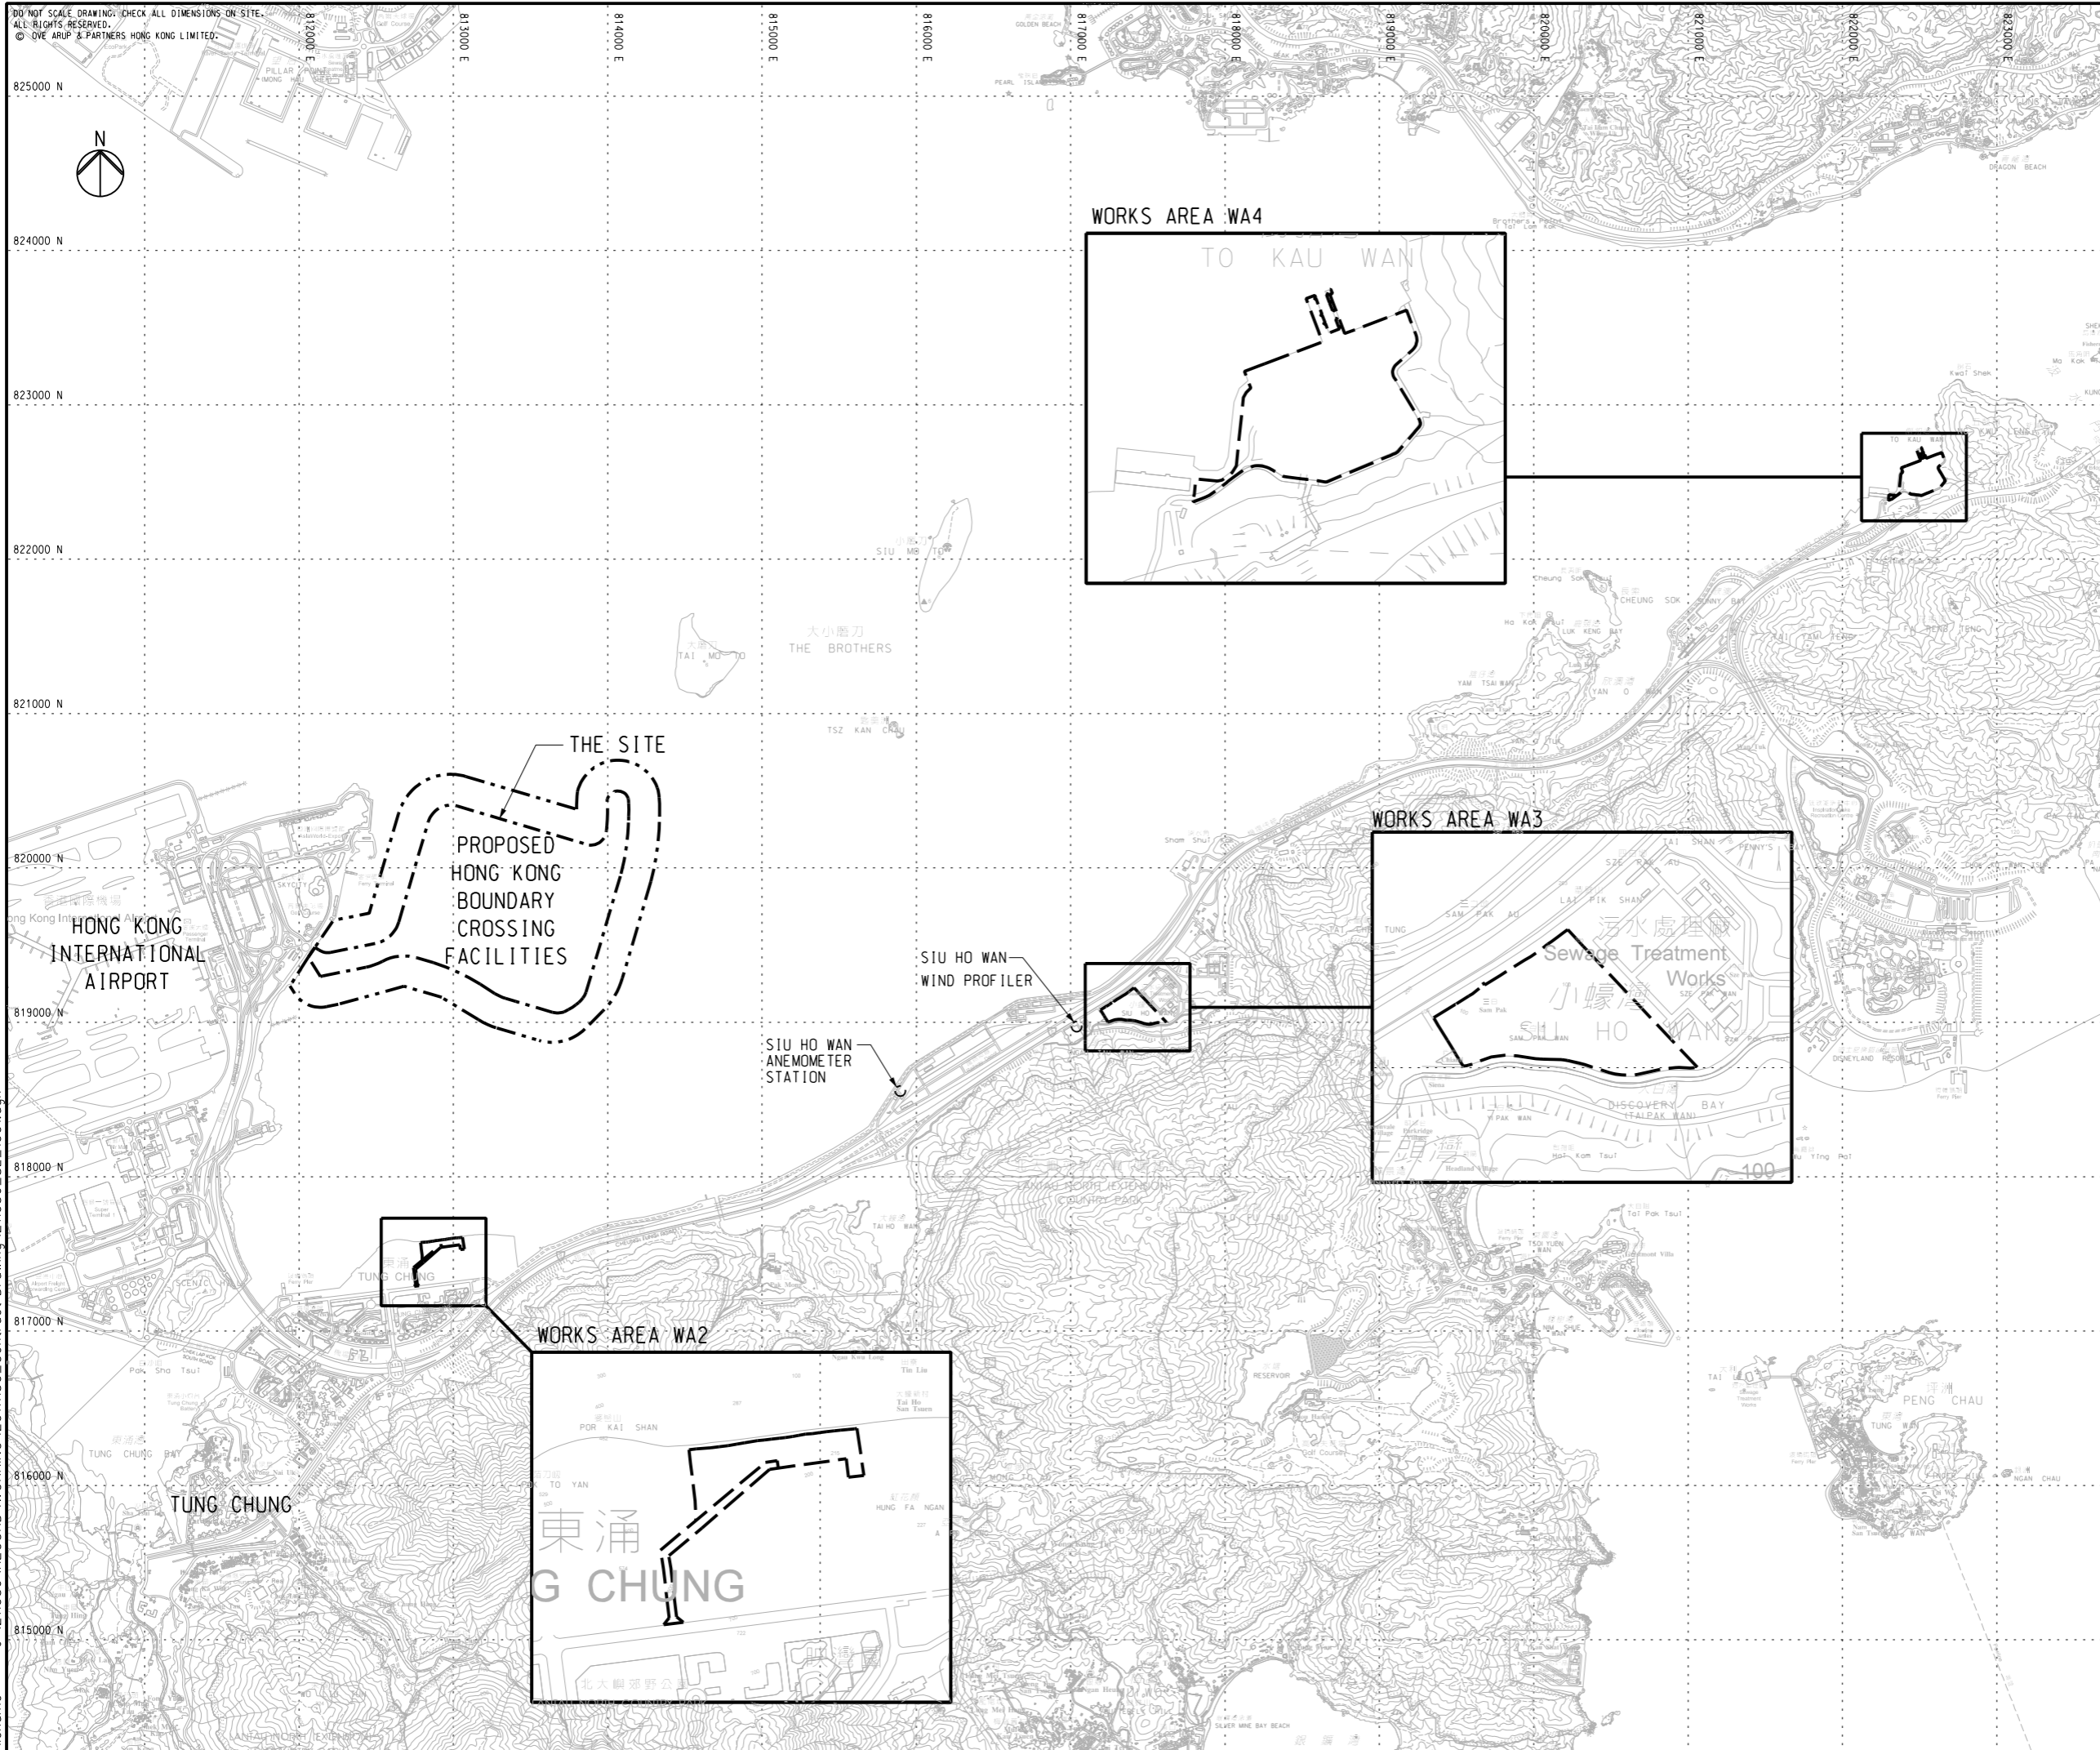

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

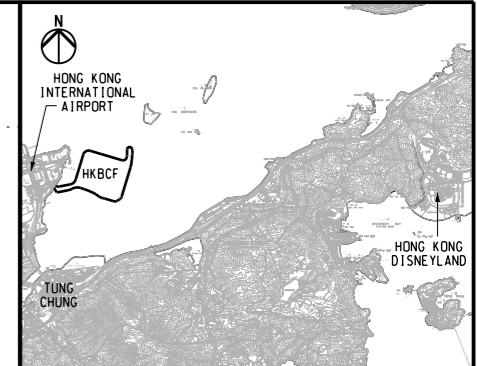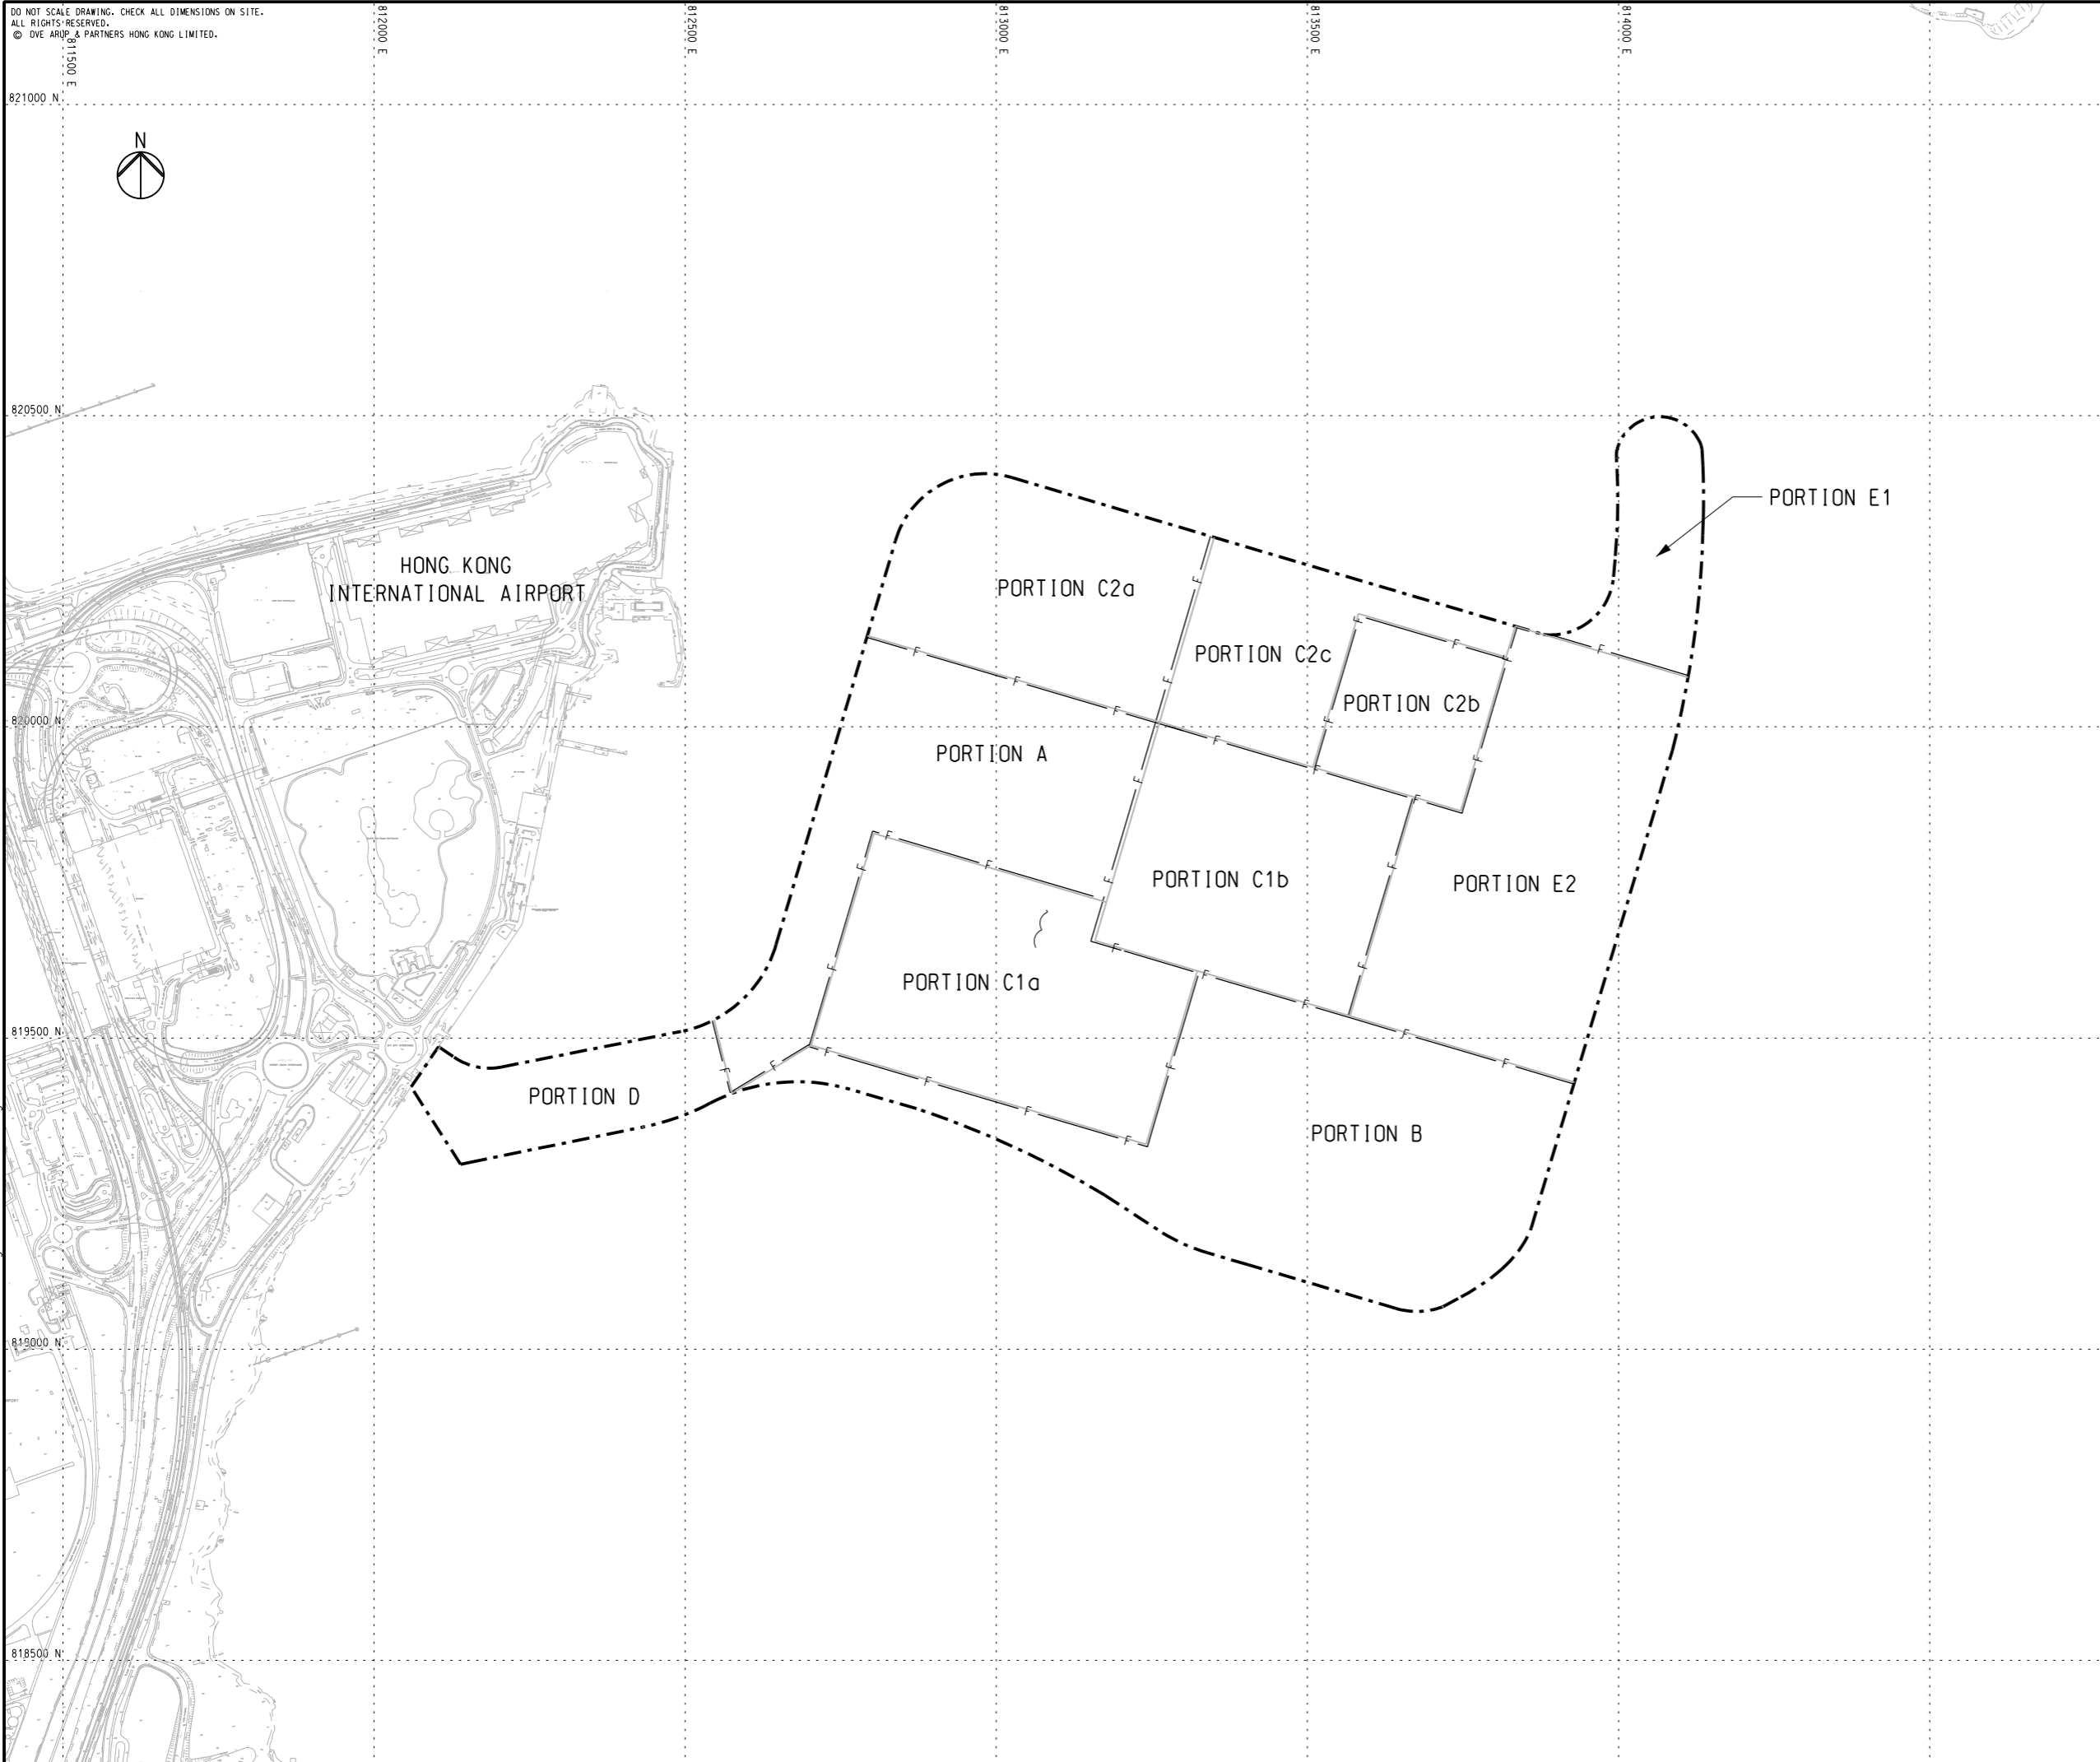

KEY PLAN

- NOTES**
- FOR LEGENDS AND NOTES FOR CHAIN LINK FENCE AND GATE REFER TO DRG NO. 211036/SL/1013.
 - THE ERECTION OF CHAIN LINK FENCE AND GATES SHALL BE COMPLETED BY THE HANDOVER DATE OF EACH PORTION OF SITE, OR AS INSTRUCTED BY THE ENGINEER.
 - FOR SETTING OUT COORDINATES OF DIFFERENT PORTIONS OF SITE REFER TO DRG NO. 211036/SL/1003.
 - ACCESS POINTS BETWEEN PORTIONS SHALL BE PROVIDED BY THE CONTRACTOR, AND THE LOCATIONS SHALL BE AGREED WITH THE ENGINEER ON SITE.
 - FOR HOARDING AND FENCE AT FILL BANK AT TSEUNG KWAN O AREA 137 REFER TO DRG NO. 211036/SL/1015.

LEGEND

	SETTING OUT LINE (SOL)
	WORKS AREA BOUNDARY
	PORTIONS BOUNDARY LINE

Rev	Description	By	Date
-	FOR CONSTRUCTION	HYJL	11/11

Consultant

ARUP	奧雅納工程顧問	●
Ove Arup & Partners Hong Kong Limited		
Supported By :	Ecosystems Ltd.	○
	EDA Marine Ltd.	○
	Geotechnical Consulting Group (Asia) Ltd.	○
	Hong Kong Cetacean Research Project	○
	Intel:Build Technyx Asia Limited	○
	Tony Gee and Partners LLP	○

Contract No. and Title:
Contract No. HY/2010/02
Hong Kong-Zhuhai-Macao Bridge
Hong Kong Boundary Crossing Facilities
- Reclamation Works


Drawing title
WORKS AREA LAYOUT
AND HOARDING PLAN
(SHEET 2 OF 3)

Drawing no. 211036/SL/1014		Rev. -	
Drawn RL	Date 06/10	Checked KKY	Approved DML
Scale 1:5000 @A1 1:10000 @A3		Status WORKING	


COPYRIGHT RESERVED

路政署
HIGHWAYS DEPARTMENT
 港珠澳大橋香港工程管理局
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office

Printed by : 12/17/2011
 Filename : J:\211036\RECORD\WORKING\20111130_Contract Drawing_211036_SL_1014.dgn

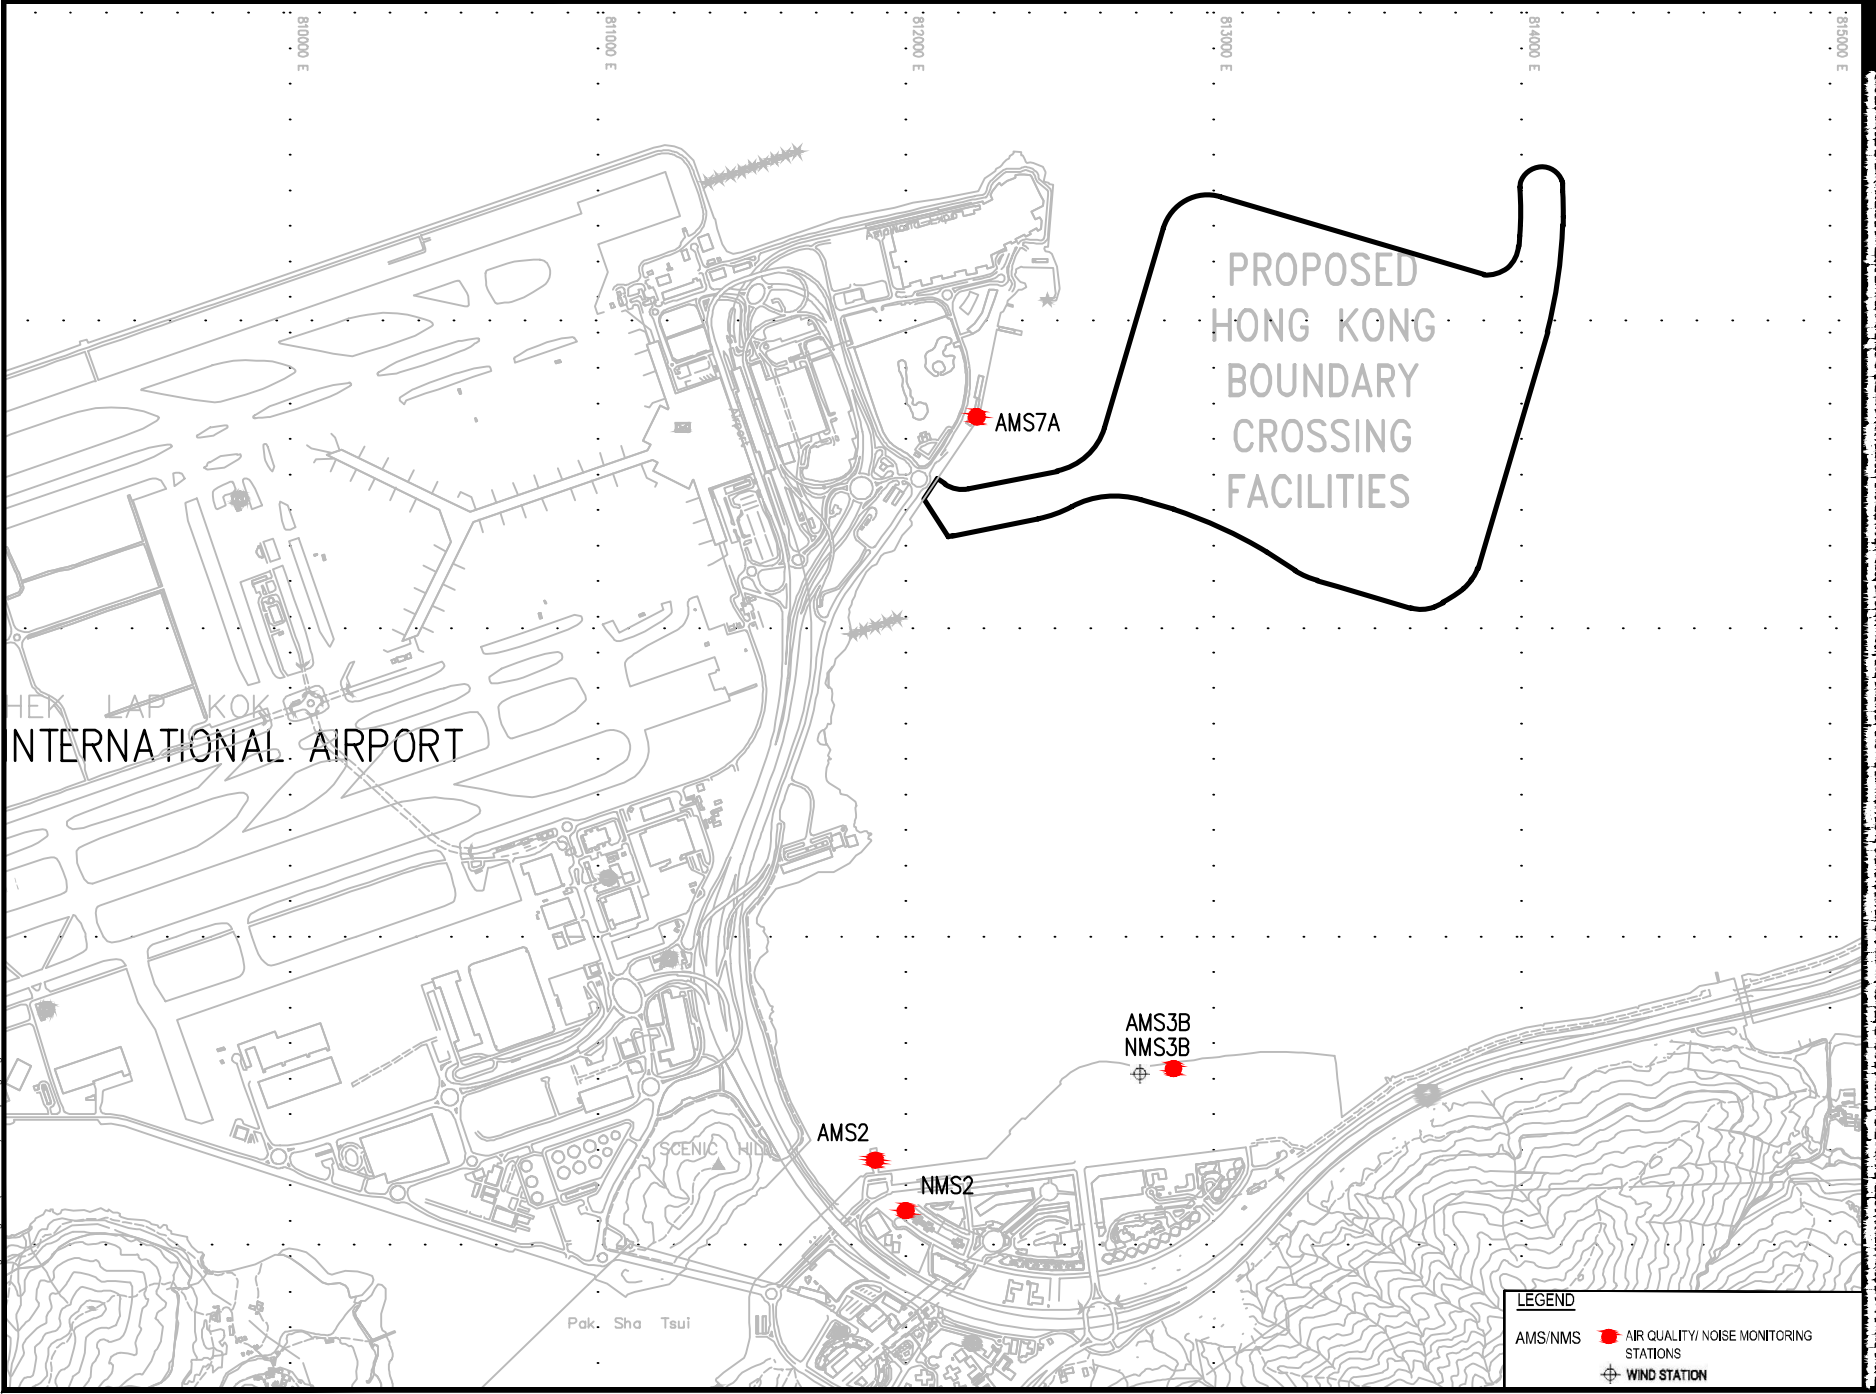

LEGEND	
AMS/NMS	AIR QUALITY/ NOISE MONITORING STATIONS
	WIND STATION

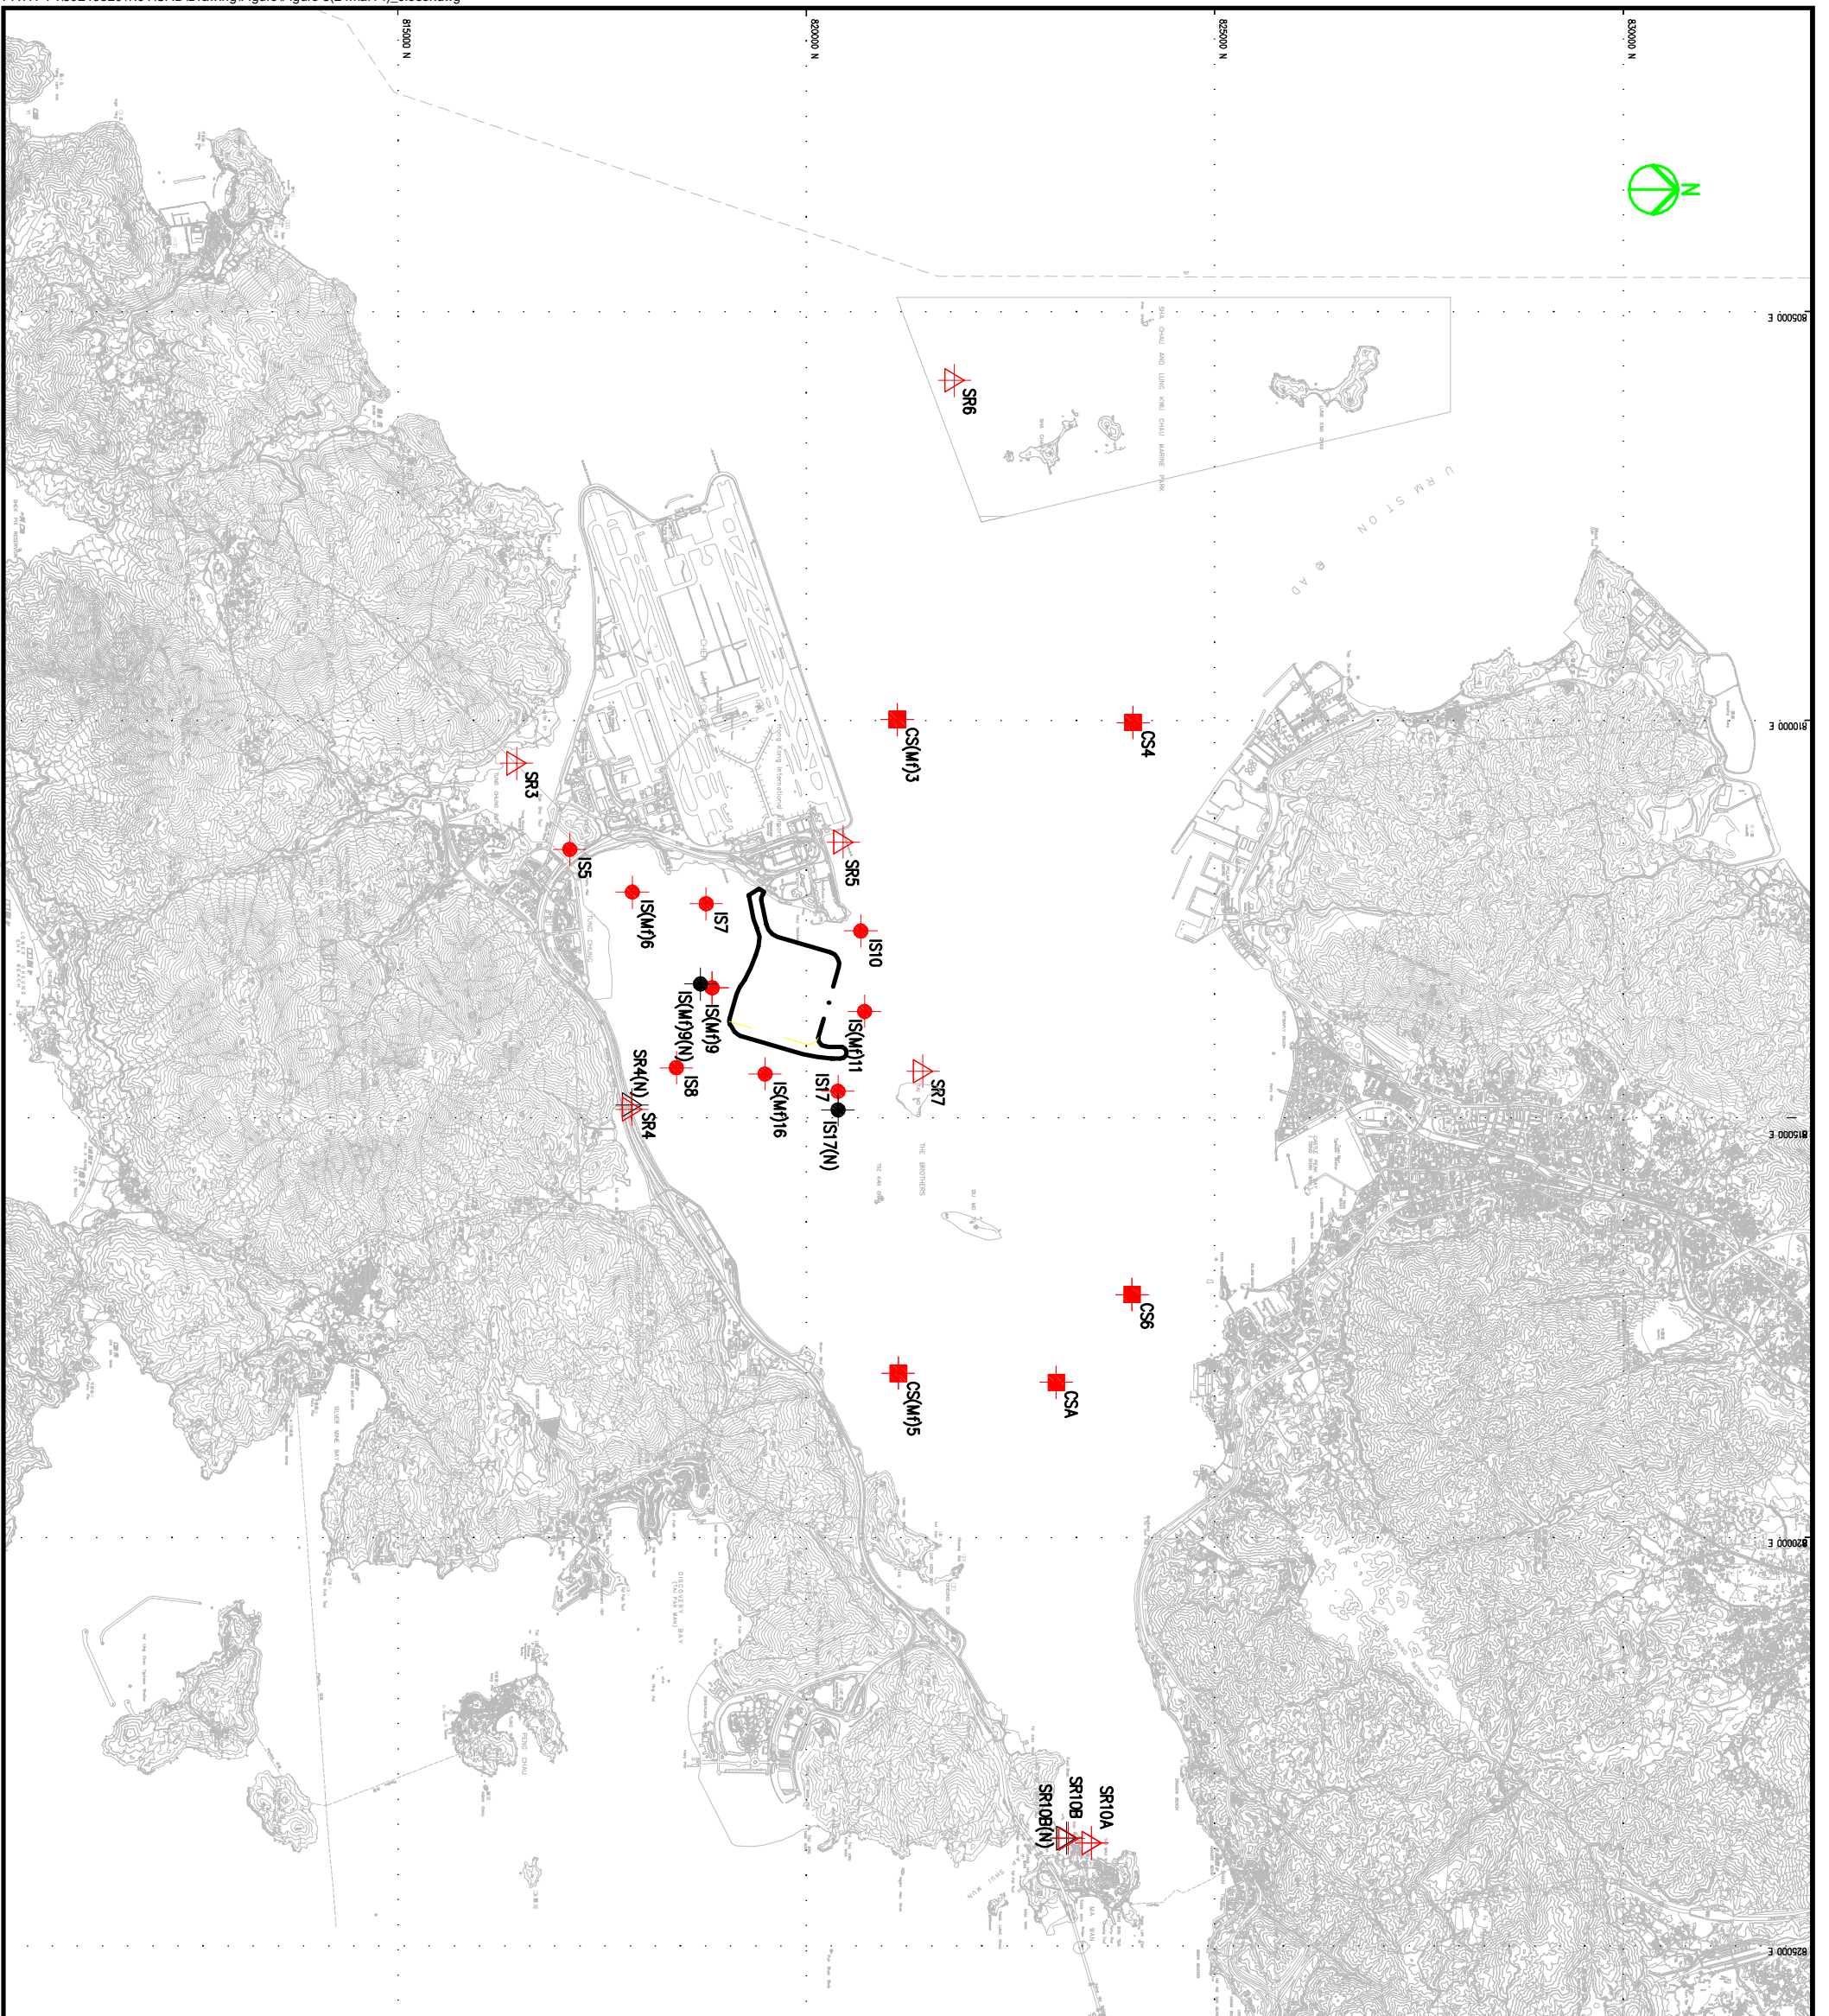


LEGEND

- IS (Red circle with dot) IMPACT STATIONS
- CS (Red square) CONTROL / FAR FIELD STATIONS
- SR (Red triangle) SENSITIVE RECEIVERS STATIONS
- SR (Black triangle) SENSITIVE RECEIVERS STATIONS (RELOCATED)
- IS (Black circle with dot) IMPACT STATIONS (RELOCATED)

SETTING OUT SCHEDULE

MONITORING STATIONS	CO-ORDINATES	
	EASTING	NORTHING
IS5	811579	817106
IS(M)16	812101	817873
IS7	812244	818777
IS8	814251	818412
IS(M)9	813273	818850
IS(M)9(N)	813226	818708
IS10	812577	820670
IS(M)11	813562	820716
IS(M)16	814328	819497
IS17	814539	820391
IS17(N)	814767	820391
SR3	810525	816456
SR4(N)	814705	817859
SR5	811489	820455
SR6	805837	821818
SR7	814293	821431
SR10A	823741	823495
SR10B(N)	823683	823187
CS(M)3	809989	821117
CS(M)5	817990	821129
CS4	810025	824004
CS6	817028	823992
CSA	818103	823064

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and disclaims any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

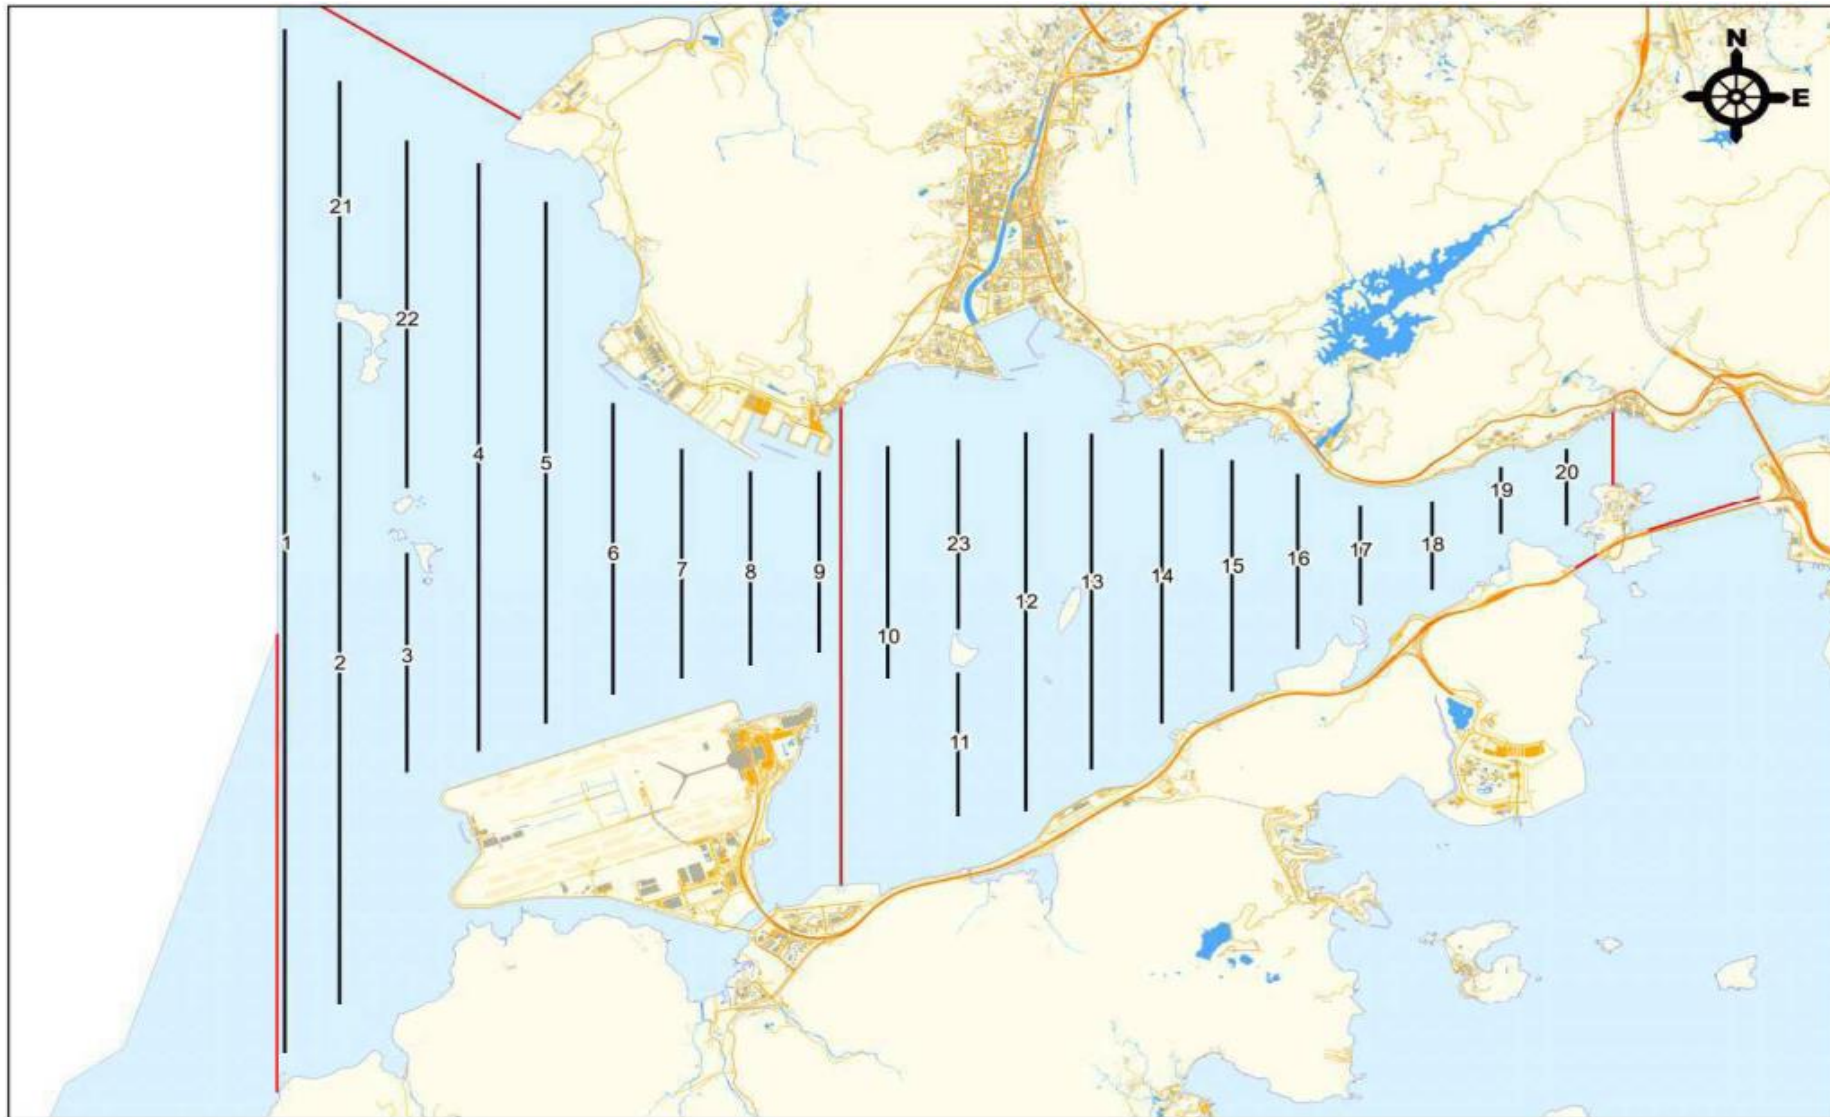


Remarks:

*Transect 10 is now 3.6km in length due to the HKBCF construction site.

^Coordinates for transect lines 1, 2, 7, 8, 9 and 11 have been updated in respect to the Proposal for Alteration of Transect Line for Dolphin Monitoring approved by EPD on 19 August 2015. The total transect length for both NEL and NWL combined is 108km.


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

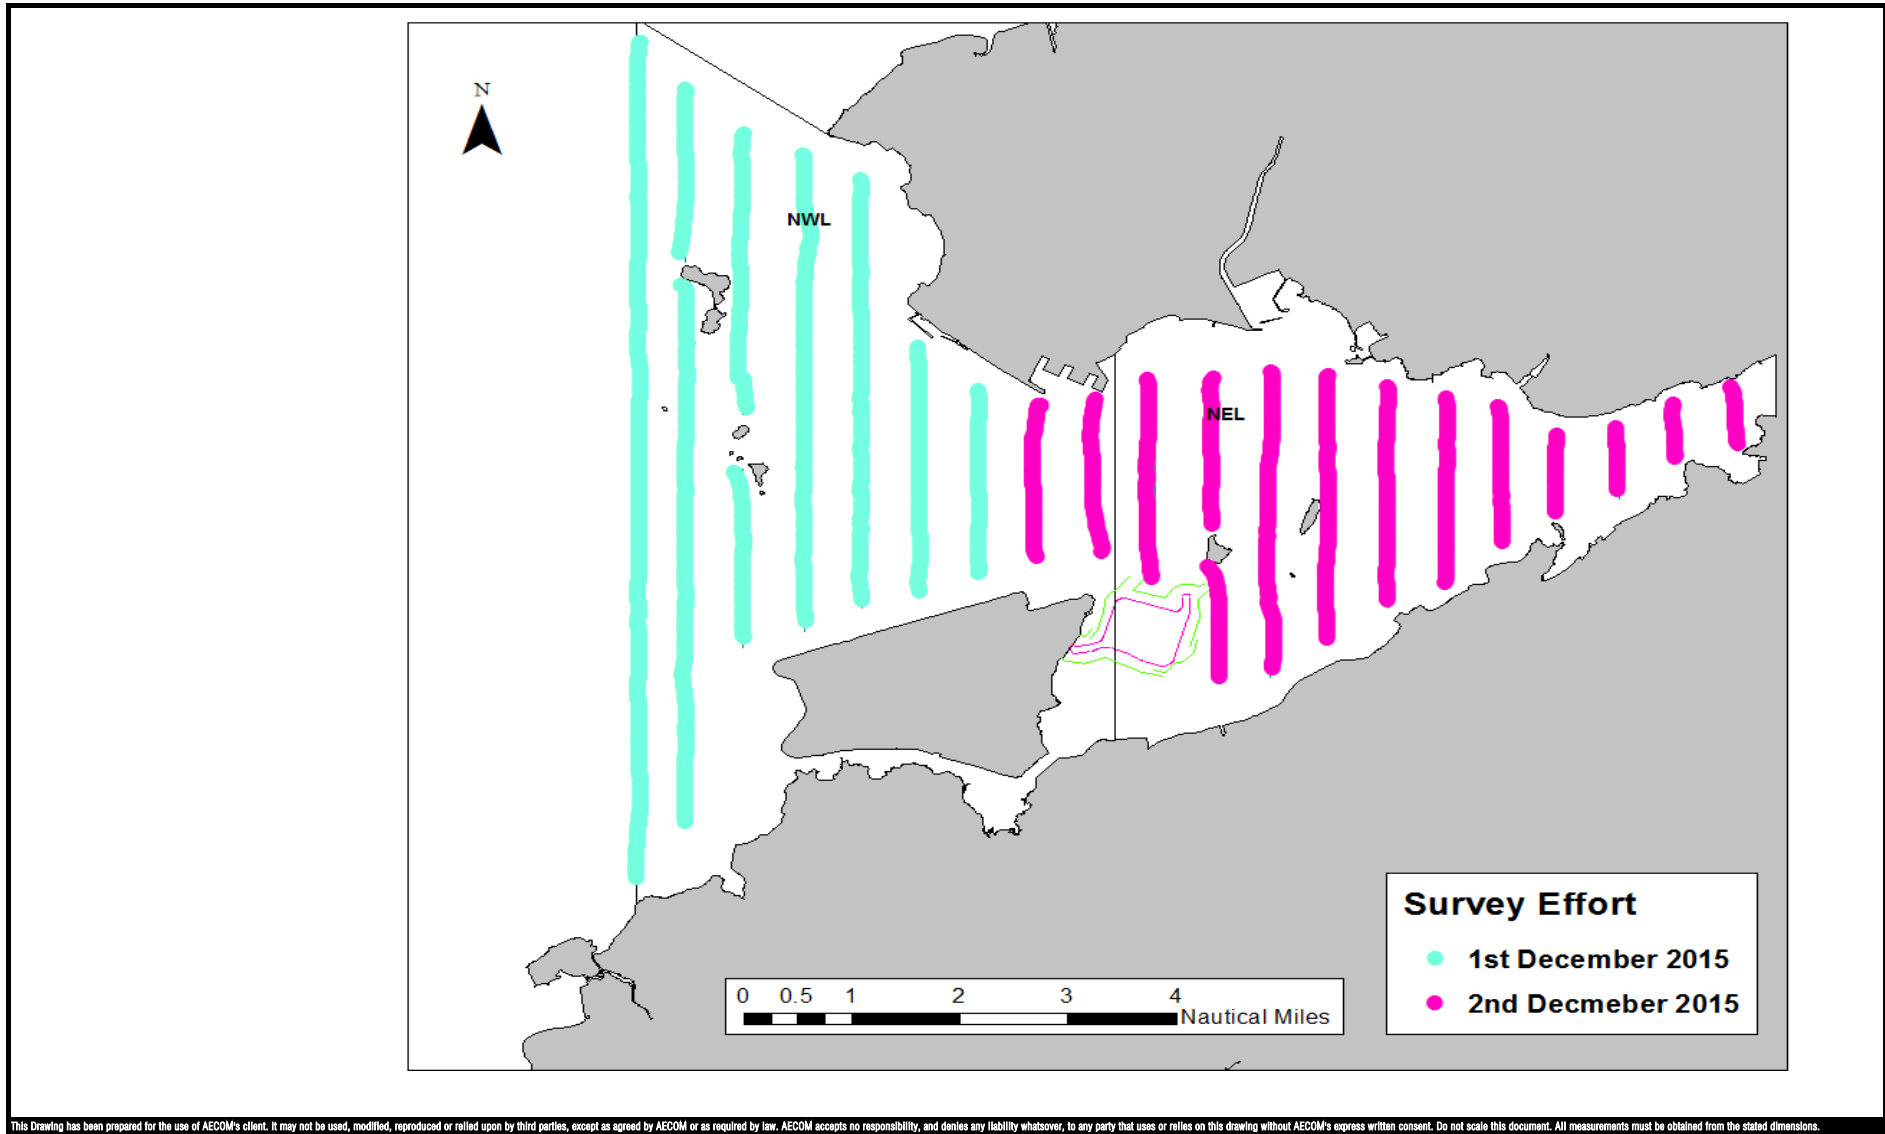

**HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS**
 Project No.: 60249820 Date: Jan 2016

**Impact Dolphin Monitoring Survey Efforts
 on 1 & 2 December 2015**

Figure 5a

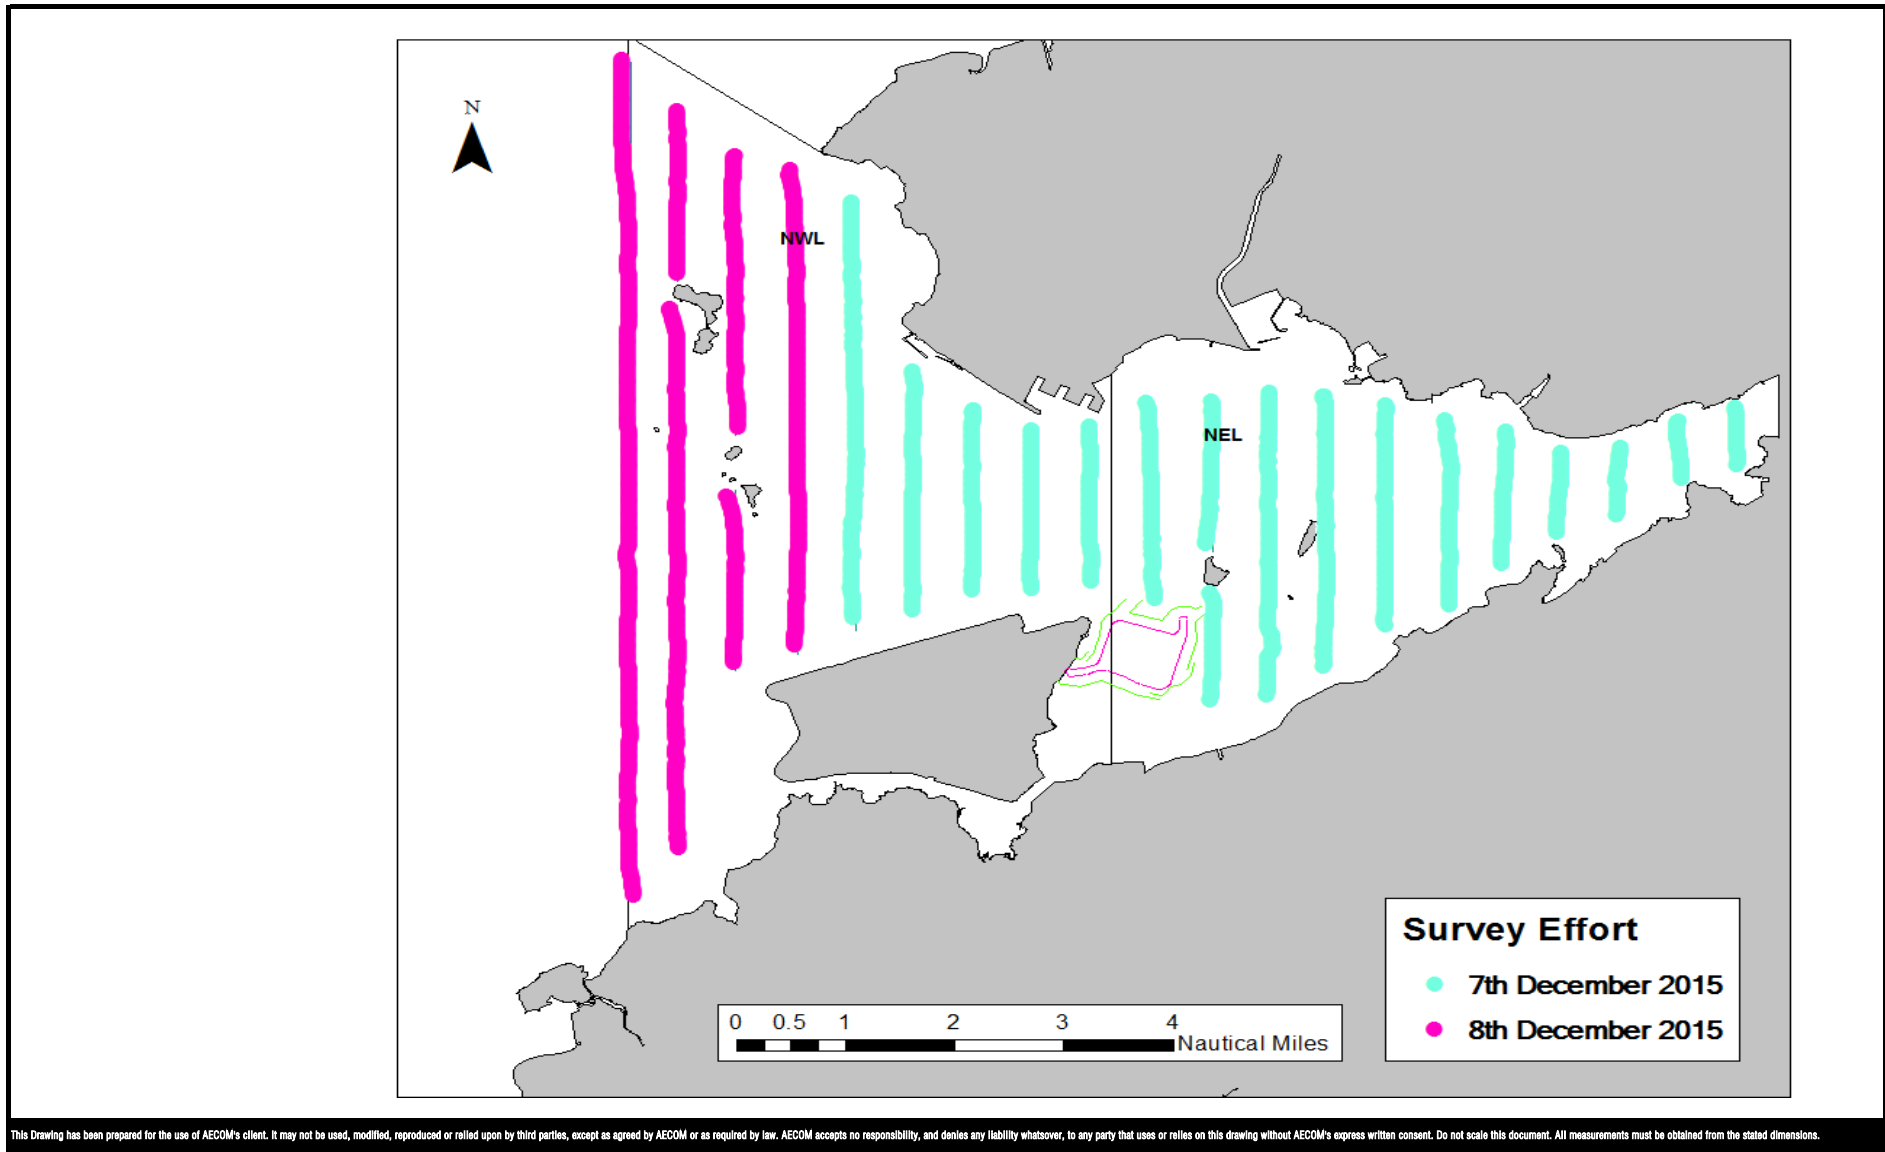


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: Jan 2016

Impact Dolphin Monitoring Survey Efforts
on 7 and 8 December 2015


Figure 5b

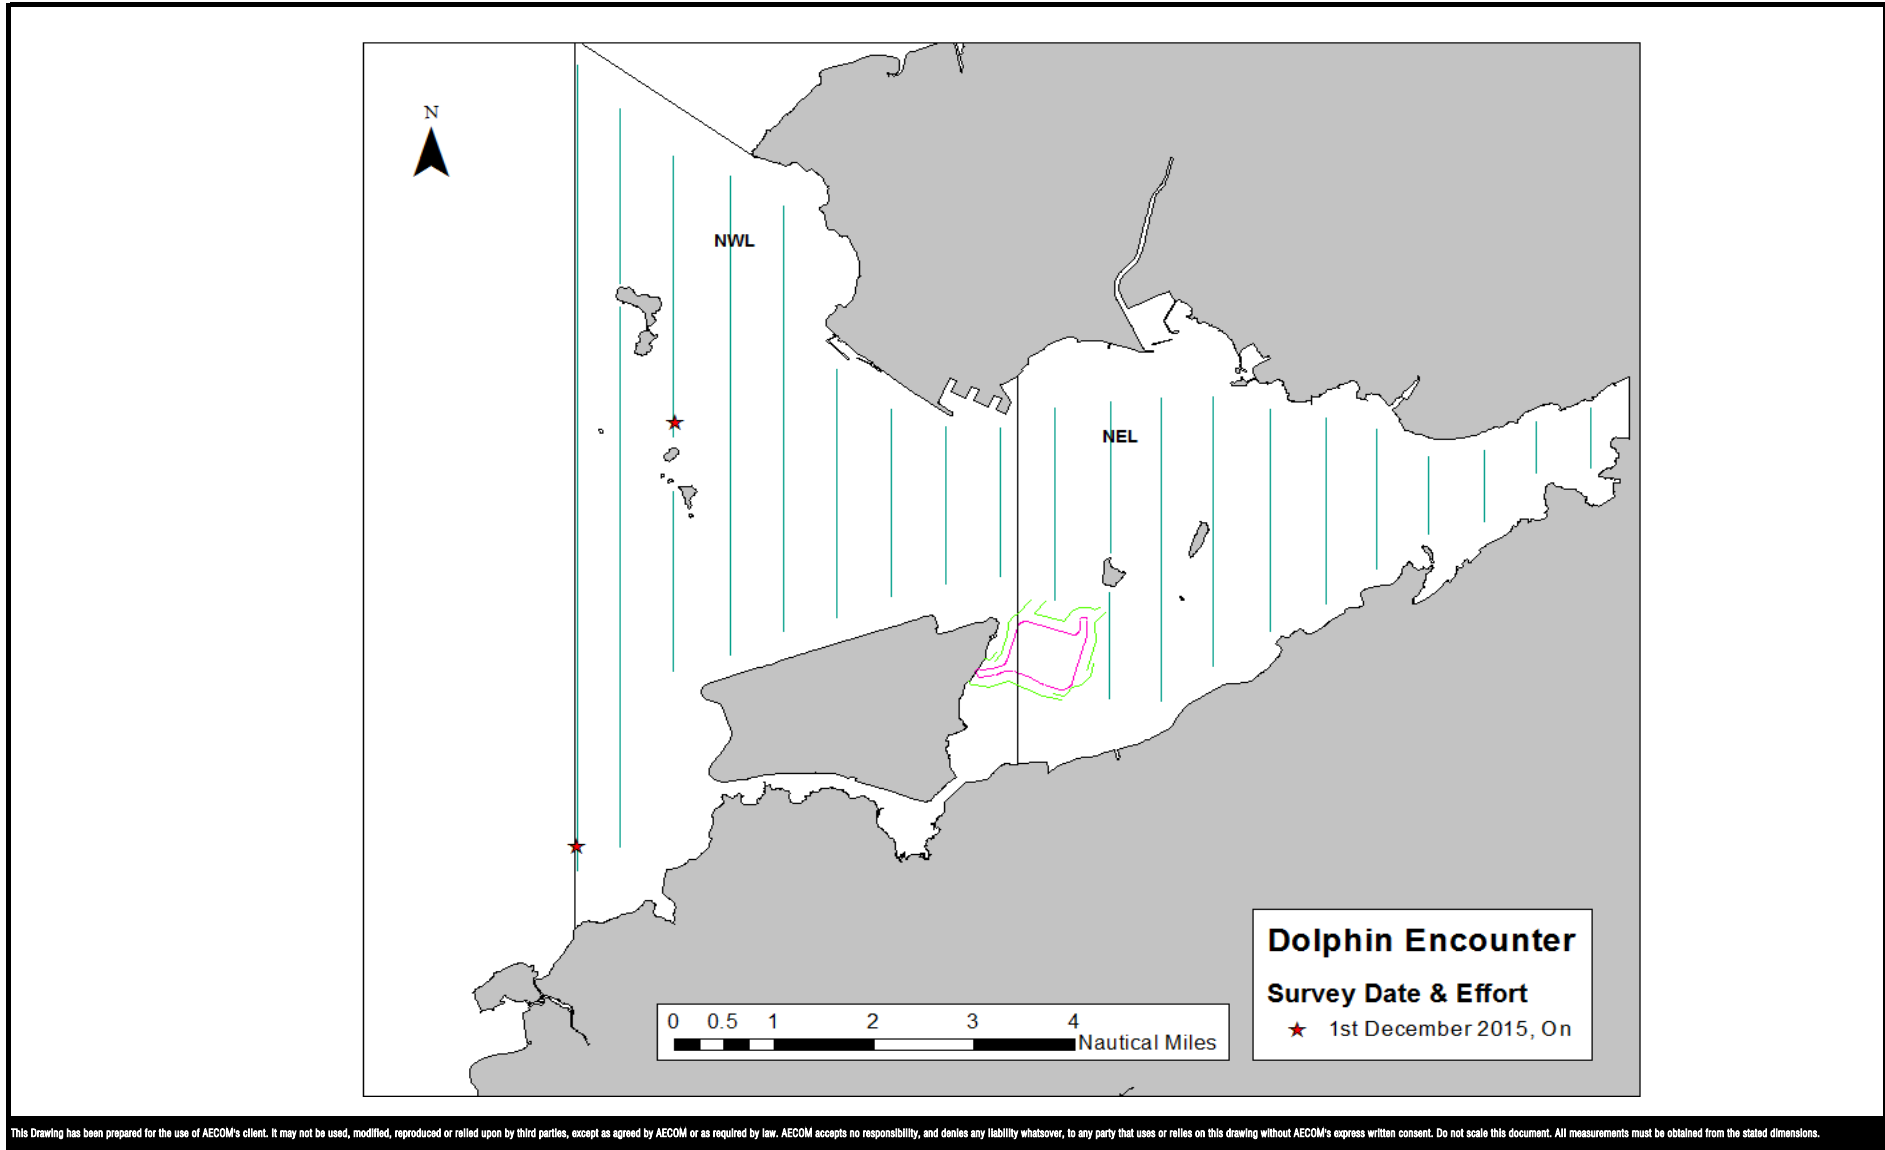

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: Jan 2016

Impact Dolphin Monitoring Survey
Sightings in December 2015


Figure 5c

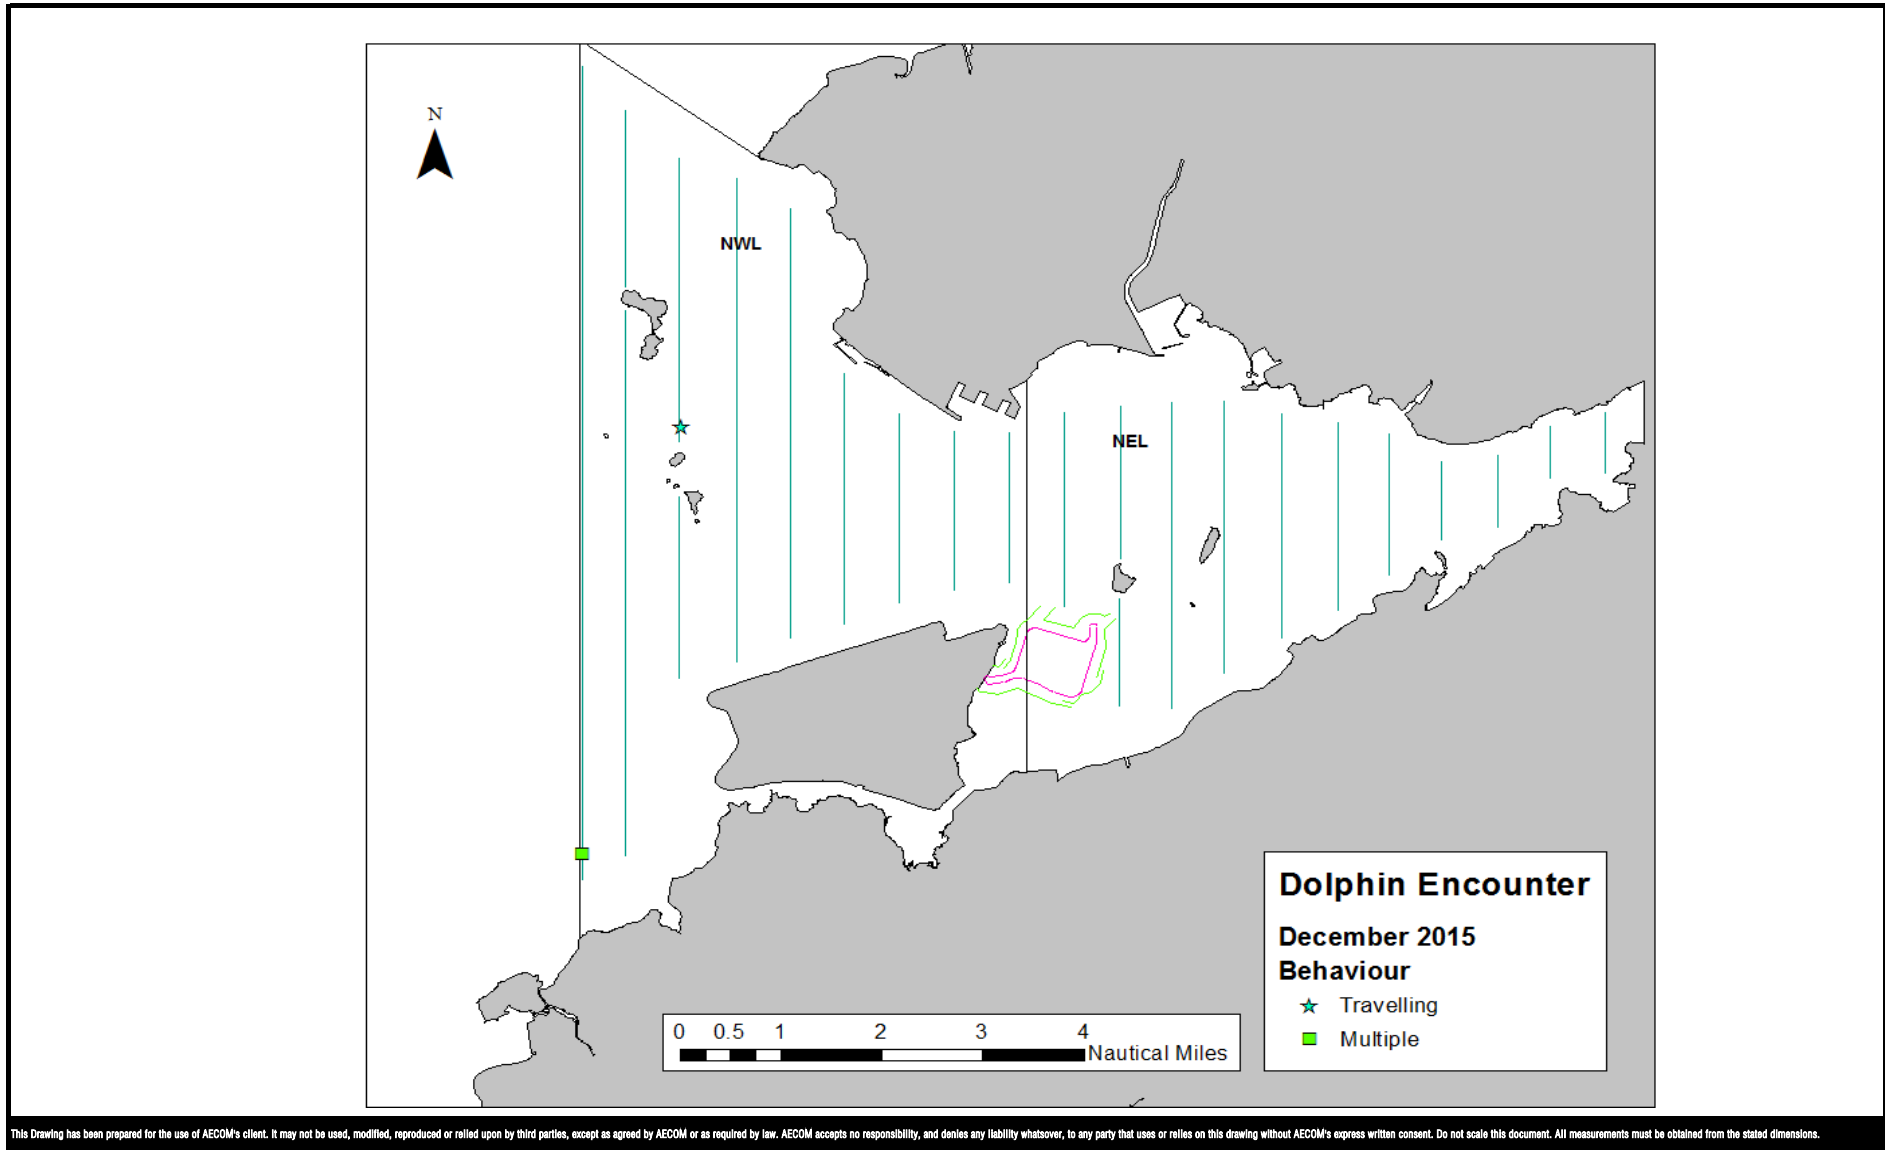


**HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS**
 Project No.: 60249820 Date: Jan 2016

**Impact Dolphin Monitoring Survey
 Behaviour Map in December 2015**

Figure 5d

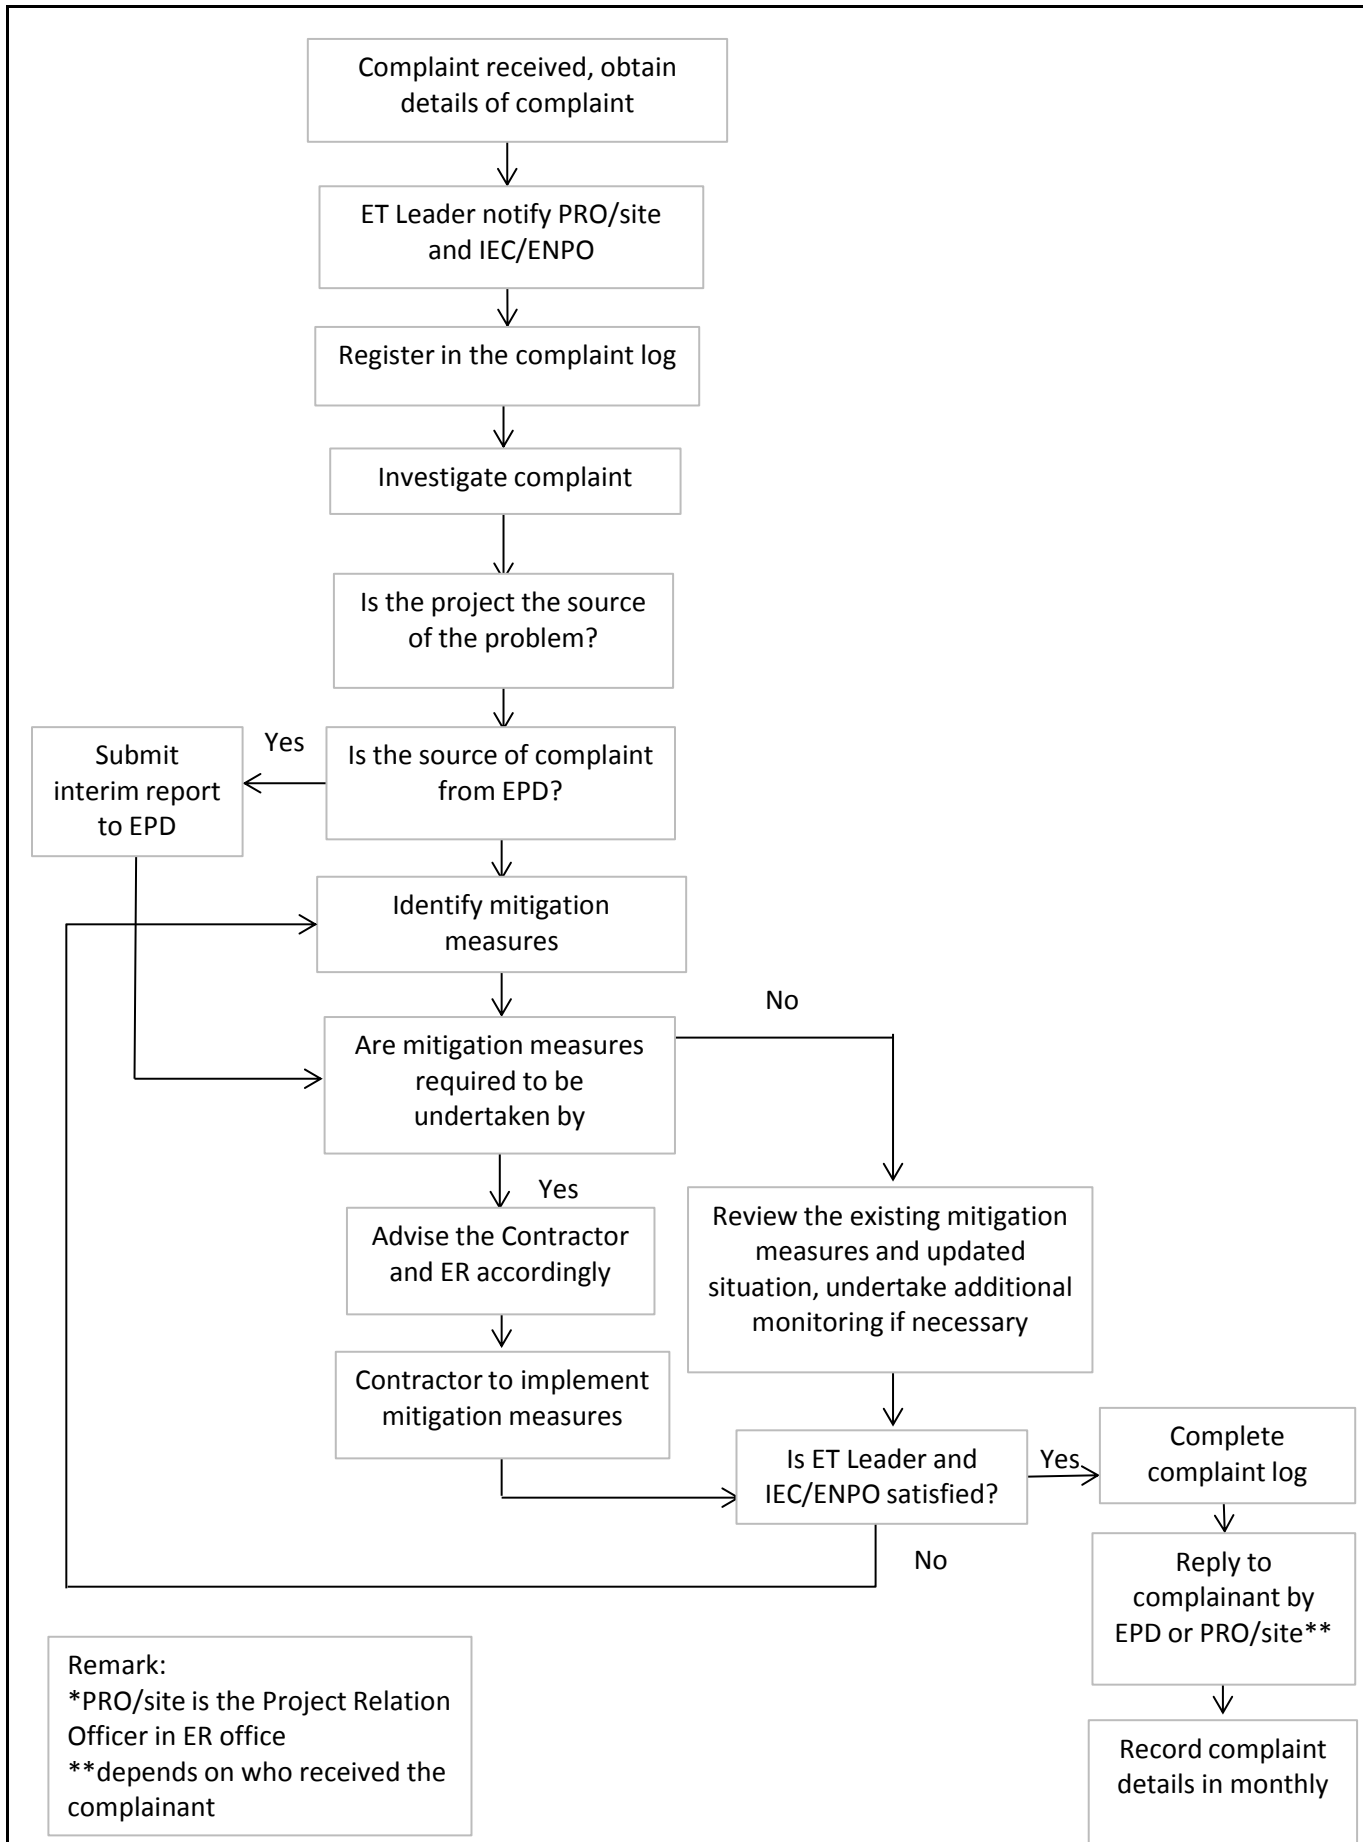

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

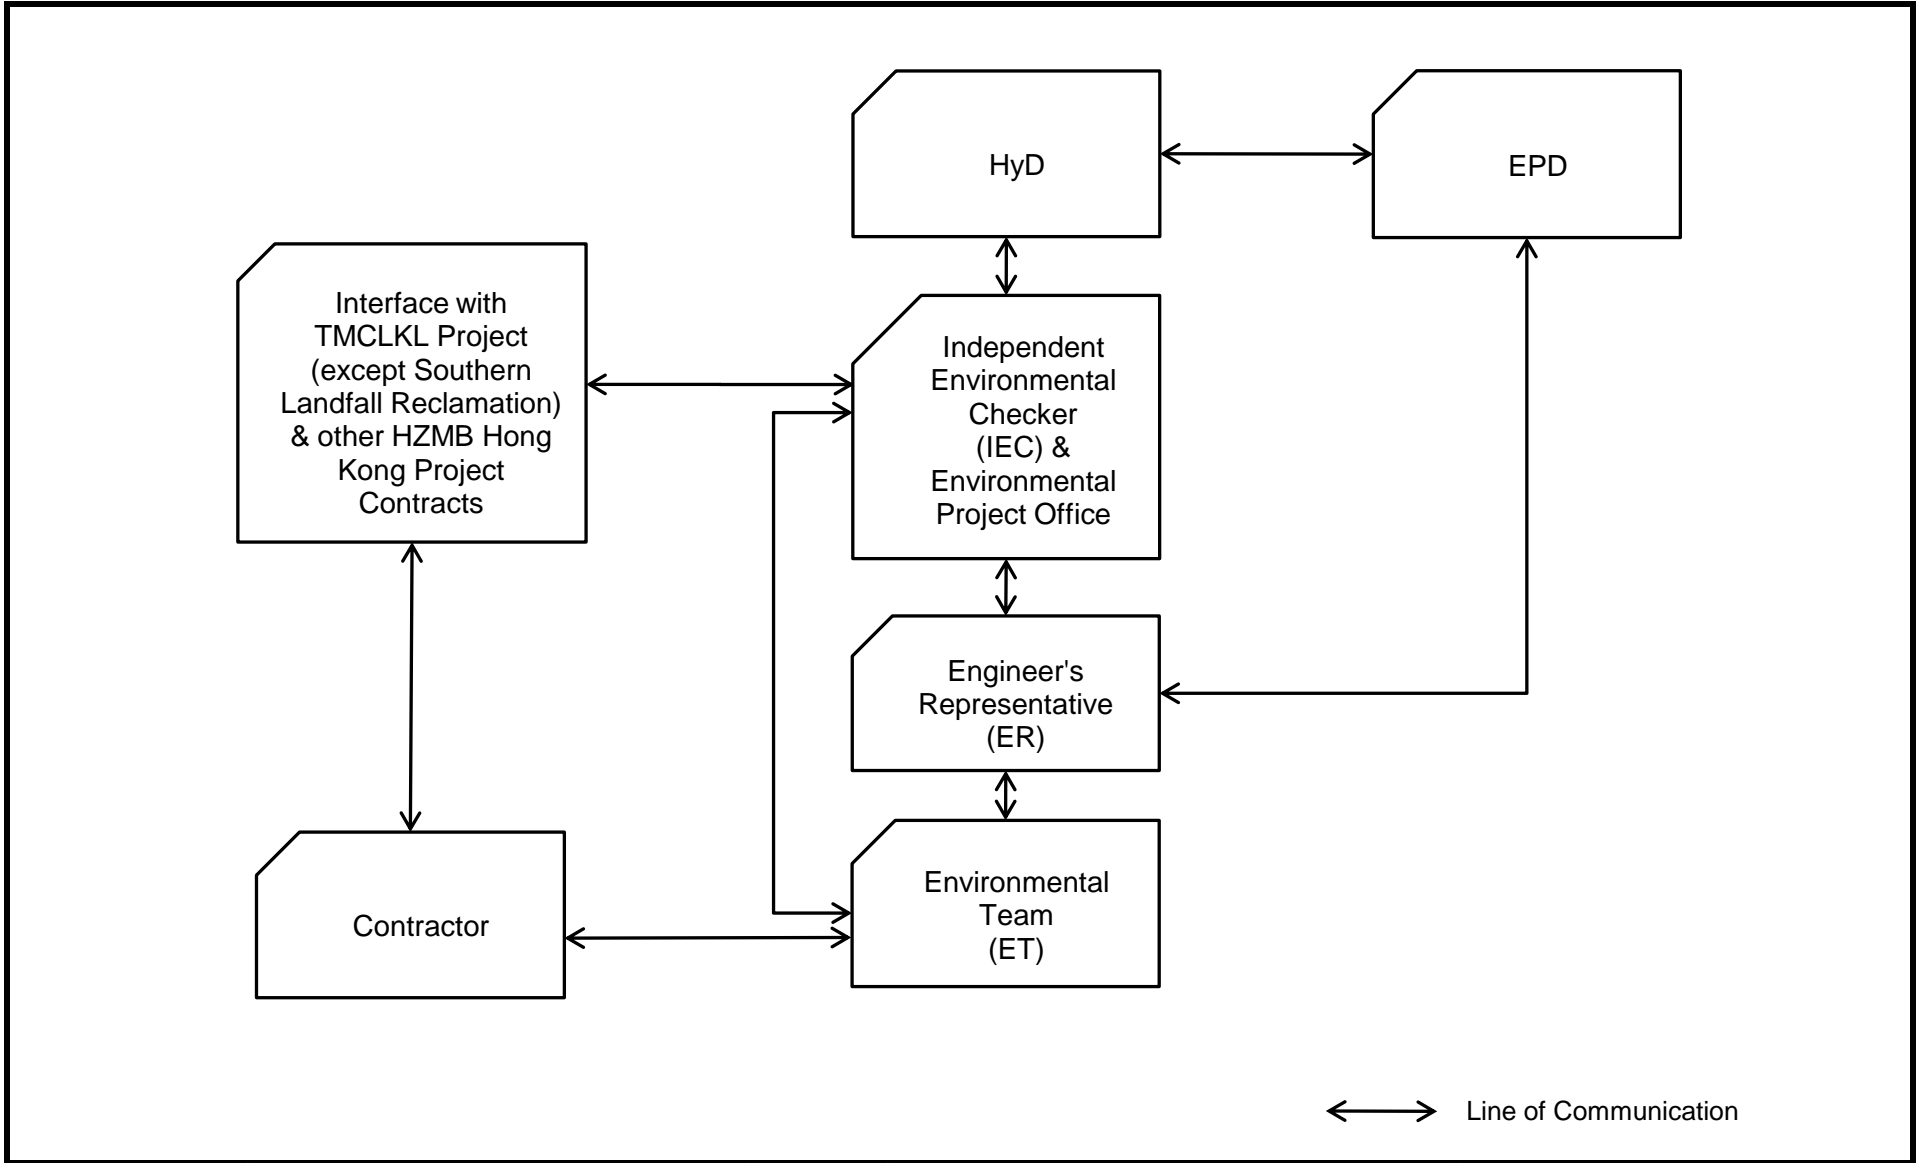

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			

49th_7 Monthly Progress Report Status as on 21Dec2015															
Contract Key Dates						90	06-Dec-15 A	19-Mar-16	-73	▶					
Key Dates for achievement of Stages and completion of Sections						90	07-Dec-15 A	19-Mar-16	-73	▶					
G1065	KD-04C2 Completion of Section A Edge Area AC2 02Aug2015 SA3	0		20-Dec-15 A											
G1070	KD-05, Completion of Section D C1, C2, C3 & C4 Except Sloping outfall 10Aug2015 SA3	0		07-Dec-15 A											
G1072	KD-05, Completion of Section D EC1-1 to EC1-6 10Aug2015 SA3	0		10-Mar-16*	-213										
G1077	KD-05, Completion of Section D EC1-1 to EC1-6 West side to Other Contractors	0		18-Feb-16*	-192										
G1081	KD-06C4TM, Completion of Section BC4TM Main Area West 12Sep2014 SA4	0		31-Dec-15*	-475										
G1086	KD-06C3 Completion of SEction BC3 Main Area East-N 21Nov2015 SA4	0		25-Feb-16*	-96										
G1090	KD-07C3, Completion of Section C1aC3 6Jan2016 SA4	0		11-Jan-16*	-5										
G1092	KD-07C4, Completion of Section C1aC4 22Sep2014 SA4	0		19-Mar-16*	-544										
G1095	KD-08C3, Completion of Section C1bC3 South East 30Sep2015 SA4	0		31-Dec-15*	-92										
G1100	KD-08C3, Completion of Section C1bC3 South West 30Sep2015 SA4	0		21-Dec-15*	-81										
G1102	KD-08C3, Completion of Section C1bC3 North East 30Sep2015 SA4	0		17-Mar-16*	-169										
G1117	KD-09C2, Completion of Section C2aC2 Edge Area C104 - C109 28Nov2015 SA3 0-43M	0		31-Dec-15*	-33										
G1130	KD-11TM, Completion of Section E2TM Main Area North 05Feb2015 SA4	0		12-Jan-16*	-341										
Supplementary Agreement						90	06-Dec-15 A	19-Mar-16	-74	▶					
SA4						90	06-Dec-15 A	19-Mar-16	-74	▶					
SA4-KD06-010	KD-06C3 Completion of Section BC3 21Nov2015	0		25-Feb-16*	-97										
SA4-KD06-020	KD-06C8E Completion of Section BC8E 17Jun2015	0		25-Feb-16*	-254										
SA4-KD06-030	KD-06C8N Completion of Section BC8N 17Jun2015	0		25-Feb-16*	-254										
SA4-KD06-040	KD-06C8NE Completion of Section BC8NE 17Jun2015	0		25-Feb-16*	-254										
SA4-KD07-010	KD-07C3 Completion of Section C1aC3 6Jan2016	0		11-Jan-16*	-6										

<ul style="list-style-type: none"> — Remaining Level of Effort ◆ Milestone — Actual Level of Effort ▼ Summary — Actual Work — Remaining Work — Critical Remaining Work 	<p>49th_7 Monthly Progress Report Status as on 21Dec2015</p> <p>Page 1 of 25</p>	<p>TASK filters: No Option 1 2, Three Month Rolling.</p> <p style="text-align: right;"><i>Primavera Systems, Inc.</i></p>
---	--	---

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015	2016			
						Dec	Jan	Feb	Mar	
						49	50	51	52	
SA4-KD07-020	KD-07C4 Completion of Section C1aC4 22Sep2014	0		19-Mar-16*	-545					
SA4-KD08-010	KD-08C3 Completion of Section C1bC3 30Sep2015	0		31-Dec-15*	-93					
SA4-KD08-020	KD-08C8NE Completion of Section C1bC8NE 17Jul2015	0		31-Dec-15*	-168					
SA4-KD08-030	KD-08C8NW Completion of Section C1bC8NW 17Jul2015	0		06-Dec-15 A						
SA4-KD08-040	KD-08C8SE Completion of Section C1bC8SE 17Jul2015	0		31-Dec-15*	-168					
SA4-KD09-020	KD-09C1C3 Completion of Section C2aC1C3 19Dec2015	0		25-Feb-16*	-69					
Summary Programme		90	06-Dec-15 A	19-Mar-16	-73	▶				
Portion Summary		90	06-Dec-15 A	19-Mar-16	-73	▶				
Portion A		0	20-Dec-15 A	20-Dec-15 A		▶				
ZG1065	KD-04C2 Completion of Section A Edge Area AC2 2Aug2015 SA3	0		20-Dec-15 A						
ZG1067	KD-04C2 Completion of Section A Main Area South AC2 2 Aug2015 SA3	0		20-Dec-15 A						
ZGA3-KD04-020	KD-04C2 Completion of Section AC2 2Aug2015	0		20-Dec-15 A						
Portion B		56	31-Dec-15	25-Feb-16	-96	▶				
ZG1081	KD-06C4TM, Completion of Section BC3 Main Area West 21Nov2015 SA4	0		31-Dec-15*	-40					
ZG1086	KD-06C3 Completion of SEction BC3 Main Area East-N 21Nov2015 SA4	0		25-Feb-16*	-96					
ZGA4-KD06-010	KD-06C3 Completion of Section BC3 21Nov2015	0		25-Feb-16*	-97					
ZGA4-KD06-020	KD-06C8E Completion of Section BC8E 17Jun2015	0		25-Feb-16*	-254					
ZGA4-KD06-030	KD-06C8N Completion of Section BC8N 17Jun2015	0		25-Feb-16*	-254					
ZGA4-KD06-040	KD-06C8NE Completion of Section BC8NE 17Jun2015	0		25-Feb-16*	-254					
Portion C		90	06-Dec-15 A	19-Mar-16	-73	▶				
Portion C1a		68	11-Jan-16	19-Mar-16	-73	▶				
ZG1090	KD-07C3, Completion of Section C1aC3 6Jan2016 SA4	0		11-Jan-16*	-5					
ZG1092	KD-07C4, Completion of Section C1aC4 22Sep2014 SA4	0		19-Mar-16*	-544					

Remaining Level of Effort Milestone
 Actual Level of Effort Summary
 Actual Work
 Remaining Work
 Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016								
						Dec		Jan		Feb		Mar						
						49	50	51	52	53	54	55	56					
ZGA4-KD07-010	KD-07C3 Completion of Section C1aC3 6Jan2016	0		11-Jan-16*	-6													
ZGA4-KD07-020	KD-07C4 Completion of Section C1aC4 22Sep2014	0		19-Mar-16*	-545													
Portion C1b		88	06-Dec-15 A	17-Mar-16	-169													
ZG1095	KD-08C3, Completion of Section C1bC3 South East 30Sep2015 SA4	0		31-Dec-15*	-92													
ZG1100	KD-08C3, Completion of Section C1bC3 South West 30Sep2015 SA4	0		06-Dec-15 A														
ZG1102	KD-08C3, Completion of Section C1bC3 North East 30Sep2015 SA4	0		17-Mar-16*	-169													
ZGA4-KD08-020	KD-08C8NE Completion of Section C1bC8NE 17Jul2015	0		17-Mar-16*	-245													
ZGA4-KD08-030	KD-08C8NW Completion of Section C1bC8NW 17Jul2015	0		06-Dec-15 A														
ZGA4-KD08-040	KD-08C8SE Completion of Section C1bC8SE 17Jul2015	0		31-Dec-15*	-168													
Portion C2a		0	25-Feb-16	25-Feb-16	-69													
ZGA4-KD09-020	KD-09C1C3 Completion of Section C2aC1C3 19Dec2015	0		25-Feb-16*	-69													
Portion D		41	29-Jan-16	10-Mar-16	-213													
ZG1070	KD-05, Completion of Section D C1, C2, C3 & C4 Except Sloping outfall 10Aug2015 SA3	0		05-Mar-16*	-208													
ZG1072	KD-05, Completion of Section D EC1-1 to EC1-6 10Aug2015 SA3	0		10-Mar-16*	-213													
ZG1074	KD-05, Completion of Section D Vertical Seawall 10Aug2015 SA3	0		29-Jan-16*	-172													
Work Zone, as defined in PS Clause 1.03(6)		426	21-Jul-15 A	18-Sep-16	578													
Portion A, B, C & E		426	21-Jul-15 A	18-Sep-16	578													
Portion A, B, C & E		426	21-Jul-15 A	18-Sep-16	578													
Seawall		383	02-Sep-15 A	18-Sep-16	578													
Optimizing Rubble Mound Seawalls		172	06-Nov-15 A	25-Apr-16	724													
Seawall Portion A at C121 - C134		172	06-Nov-15 A	25-Apr-16	724													
RFA0-010	PA at C121 - C134 Removal of Temporary Rockfill (170,000m3, 1,500m3/day)	114	06-Nov-15 A	28-Mar-16	724													
RFA0-020	PA at C121 - C134 Underlayer (21,600m3 1,000m3/day)	98	05-Jan-16	11-Apr-16	724													

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary








49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
RFA0-030	PA at C121 - C134 Rock Armour (1-3ton 30,840m3 & 0.3-1ton 14,466m3 244m3/day)	98	19-Jan-16	25-Apr-16	724				
Conforming Sloping Seawalls		383	02-Sep-15 A	18-Sep-16	578				
Rock Armour		383	02-Sep-15 A	18-Sep-16	578				
Portion B At K028 - K039 (Ch1102 - Ch1600)		203	02-Sep-15 A	22-Mar-16	758				
RFB1-030	PB at K028 - K039 on cells Rock Armour 0.3-1ton 13,505m3 237m3/day	89	18-Sep-15 A	14-Jan-16	826				
RFB1-040	PB at K028 - K039 in front of cells Removal of temporary rockfill 10205m3 190m3/day	86	02-Sep-15 A	26-Dec-15	471				
RFB1-050	PB at K028 - K039 in front of cells Geotextile & Underlayer 10-60kg 15m/day	33	27-Dec-15	28-Jan-16	758				
RFB1-060	PB at K028 - K039 in front of cells Rock Armour 0.3-1ton 11,244m3 244m3/day	54	29-Jan-16	22-Mar-16	758				
Portion E2 At K049 - C067 (Ch1990 - Ch2800)		343	12-Oct-15 A	18-Sep-16	471				
RFE2-012	PE2 at K049 - K067 on cells Removal of temporary rockfill	84	12-Oct-15 A	03-Jan-16	545				
RFE2-014	PE2 at K049 - K067 on cells Geotextile & Underlayer 10-60kg 11,733m3 200m3/day	84	17-Oct-15 A	08-Jan-16	540				
RFE2-030	PE2 at K049 - K067 on cells Rock Armour 1-3ton 31,820m3 237m3/day	134	21-Dec-15*	02-May-16	540				
RFE2-040	PE2 at K049 - K067 in front of cells Removal of temporary rockfill 25,648m3	227	27-Dec-15	09-Aug-16	471				
RFE2-050	PE2 at K049 - K067 in front of cells Geotextile & Underlayer 10-60kg 15m/day	227	16-Jan-16	29-Aug-16	471				
RFE2-060	PE2 at K049 - K067 in front of cells Rock Armour 1-3ton 32,060m3 237m3/day	227	05-Feb-16	18-Sep-16	471				
Portion E1 At C068 - C076 (Ch2800 - Ch3160)		35	04-Jan-16	07-Feb-16	653				
RFE1a-010	PE1 at K068 - K076 on cells Removal of temporary rockfill	28	04-Jan-16	31-Jan-16	653				
RFE1a-020	PE1 at K068 - K076 on cells Geotextile & Underlayer 10-60kg 5,557m3 200m3/day	28	11-Jan-16	07-Feb-16	653				
Reclamation		16	17-Nov-15 A	04-Dec-15 A					
Vertical Band Drains by Land Plant		12	17-Nov-15 A	30-Nov-15 A					
Land Portion E1 12,243nrs by Land		12	17-Nov-15 A	30-Nov-15 A					
VBDE1-10	PE1 Vertical Band Drains 3,478nrs by land plant (400nrs/day) (2HP)	12	17-Nov-15 A	30-Nov-15 A					
Earthwork Fill		16	17-Nov-15 A	04-Dec-15 A					

-  Remaining Level of Effort
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone
-  Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
Land Portion E1						16	17-Nov-15 A	04-Dec-15 A													
EFE1-010	PE1 Type D Earthwork Sand Fill upto +5.5mPD 118,263m3 5,000m3/day	16	17-Nov-15 A	04-Dec-15 A																	
Surcharge						422	21-Jul-15 A	14-Sep-16	582												
Portion A Surcharge						9	12-Dec-15 A	20-Dec-15 A													
Edge Area From SOL offset within 180m to 50m						9	12-Dec-15 A	20-Dec-15 A													
SUEA0-199	Completion of Section A at Edge Area 0 - 40m	0		20-Dec-15 A																	
CH5+110 to 5+440 Portion A North						9	12-Dec-15 A	20-Dec-15 A													
Area of 0 to 50m from Offset						9	12-Dec-15 A	20-Dec-15 A													
SUEA1-2185	PA North Area CH5+110 - CH5+440 ilssue of Surcharge Removal (Assume to start on 21Oct2015)	0		12-Dec-15 A																	
SUEA1-2190	PA North 73m-10m Surcharge Sand Removal 80,000m3 10,000m3/day	8	12-Dec-15 A	20-Dec-15 A																	
Land Portion B						352	22-Jul-15 A	07-Jul-16	-387												
Edge Areas						285	27-Sep-15 A	07-Jul-16	-671												
at K013 - K027						265	22-Nov-15 A	07-Jul-16	-677												
SUEB0-032	PB Edge Area K013-K027 Sand Surcharge Checking at +9.5mPD	10	22-Nov-15 A	14-Dec-15 A																	
SUEB0-034	PB Edge Area K013-K027 Sand Surcharge upto 10.5mPD 38,102m3 5,000m3/day	7	15-Dec-15 A	20-Dec-15 A																	
SUEB0-036	PB Edge Area K013-K027 Sand Surcharge Checking at +10.5mPD	12	21-Dec-15	01-Jan-16	-677																
SUEB0-038	PB Edge Area K013-K027 Sand Surcharge up to 11.5mPD 38,103m3 5,000m3/day by Dump Trucks	7	02-Jan-16	09-Jan-16	-582																
SUEB0-040	PB Edge Area K013-K027 Sand Surcharge Period at +11.5mPD 6mths	180	10-Jan-16	07-Jul-16	-677																
at K028 - K035						257	27-Sep-15 A	09-Jun-16	-651												
SUEB0-072	PB Edge Area K028-K035 Surcharge Strength Test Achievement	65	27-Sep-15 A	31-Dec-15	-650																
SUEB0-080	PB Edge Area K028-K035 Sand Surcharge Laying up to 11.5mPD 45,440m3 5,000m3/day	9	01-Jan-16	11-Jan-16	-557																
SUEB0-090	PB Edge Area K028-K035 Sand Surcharge Period +11.5mPD 5mths	150	12-Jan-16	09-Jun-16	-651																
at K036 - K039						213	07-Nov-15 A	06-Jun-16	-645												

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
- ▼ Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016										
						Dec		Jan		Feb		Mar								
						49	50	51	52	53	54	55	56							
SUEB0-130	PB Edge Area K036-K039 Surcharge Strength Test Achievement	24	07-Nov-15 A	31-Dec-15	-645															
SUEB0-140	PB Edge Area K036-K039 Sand Surcharge Laying up to 11.5mPD 30,293m3 5,000m3/day	7	01-Jan-16	08-Jan-16	-552															
SUEB0-150	PB Edge Area K036-K039 Sand Surcharge Period +11.5mPD 5mths	150	09-Jan-16	06-Jun-16	-645															
at K047 - K052 (w Deep Cement Mixing)		210	17-Oct-15 A	13-May-16	-616															
DCM-2070	PB Edge Area K047-K052 36-73m Surcharge Period 7mths (13May2016)	210	17-Oct-15 A	13-May-16	-616															
Reclamation Areas		219	22-Jul-15 A	25-Feb-16	-254															
SURB4-099	Completion of Section B in Reclamation Areas	0		31-Dec-15	-475															
at West of Main Area stg1		102	19-Aug-15 A	31-Dec-15	-438															
SURB1-040	PB Main Area West-S Sand Surcharge Removal 291,223m3 10,000m3/day	102	19-Aug-15 A	31-Dec-15	-438															
at West of Main Area stg2		119	01-Aug-15 A	31-Dec-15	-438															
SURB2-040	PB Main Area West-N Sand Surcharge Removal 335,714m3 10,000m3/day	119	01-Aug-15 A	31-Dec-15	-438															
at North- East of Main Area		219	22-Jul-15 A	25-Feb-16	-254															
SURB3-030	PB Main Area East-N Sand Surcharge Period +11.5mPD 7mths (16Feb2016)	210	22-Jul-15 A	16-Feb-16	-255															
SURB3-040	PB Main Area East-N Sand Surcharge Removal 60,000m3 10,000m3/day	9	17-Feb-16	25-Feb-16	-233															
Land Portion C2a		385	27-Aug-15 A	14-Sep-16	-296															
Edge Areas		385	27-Aug-15 A	14-Sep-16	-296															
Deep Cement Mixing Works at C101 - C103		270	21-Nov-15 A	12-Aug-16	-688															
DCM-3052	PC2a Edge Area C101-C103 CPT Test	8	21-Nov-15 A	28-Nov-15 A																
DCM-3060	PC2a Edge Area C101-C103 Filling up to +11.5mPD Surcharge (30m width, 14,607m3 5,000m3/day	15	30-Nov-15 A	16-Dec-15 A																
DCM-3070	PC2a Edge Area C101-C103 Surcharge Period 8mths (Land Side)	240	17-Dec-15 A	12-Aug-16	-688															
Option - Deep Cement Mixing Works at C104 - C109		385	27-Aug-15 A	14-Sep-16	-543															
DCM-4130	PC2a Edge Area C104-C109 43m width x 260m Installation 2,235nrs (Outstanding 1,175nrs, 22nrs/day from 27Oct2015)	115	27-Aug-15 A	30-Nov-15 A																
DCM-4140	PC2a Edge Area C104-C109 Hardening & Pause Period	30	01-Dec-15 A	31-Dec-15	-541															

- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- ▼ Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
DCM-4150	PC2a Edge Area C104-C109 Filling up to +5.5mPD Type D (73m width, 25,641m3) 5,000m3/day at DCM by Dump Trucks	6	21-Dec-15	26-Dec-15	-457				
DCM-4155	PC2a Edge Area C104-C109 Completion of 0-43m	0		31-Dec-15	-541				
DCM-4160	PC2a Edge Area C104-C109 Filling up to +8.5mPD Surcharge (30m width, 25,334m3 10,000m3/day at DCM by Dump Trucks	3	01-Jan-16	04-Jan-16	-461				
DCM-4162	PC2a Edge Area C104-C109 CPT Test	10	05-Jan-16	14-Jan-16	-542				
DCM-4170	PC2a Edge Area C104-C109 Filling up to +11.5mPD Surcharge (30m width, 25,334m3 10,000m3/day at DCM by Dump Trucks	3	15-Jan-16	18-Jan-16	-462				
DCM-4180	PC2a Edge Area C104-C109 Surcharge Period 8mths (Land Side) (16Sep2016)	240	19-Jan-16	14-Sep-16	-543				
at C110 - C112 Cellular Seawall		141	21-Dec-15	09-May-16	-354				
SUEC2a-010	PC2a Edge Area C110-C112 Sand Surcharge Laying up to 6.5mPD 9,385m3 5,000m3/day	2	21-Dec-15*	22-Dec-15	-301				
SUEC2a-014	PC2a Edge Area C110-C112 Sand Surcharge Laying up to 7.5mPD 9,385m3 5,000m3/day	2	23-Dec-15	24-Dec-15	-301				
SUEC2a-018	PC2a Edge Area C110-C112 Sand Surcharge Laying up to 8.5mPD 9,385m3 5,000m3/day	2	25-Dec-15	26-Dec-15	-301				
SUEC2a-020a	PC2a Edge Area C110-C112 Sand Surcharge Period at +8.5mPD 4.5mths (09May2016)	135	27-Dec-15	09-May-16	-354				
CH4+710 - CH5+110 Rubble Mound Seawall		240	14-Nov-15 A	10-Jul-16	-230				
10-73m		174	27-Nov-15 A	18-May-16	-177				
SUEC2a-1100	PC2a C113-C117 10m-73m Surcharge Strength Check as +11.5mPD	7	27-Nov-15 A	20-Dec-15 A					
SUEC2a-1110	PC2a C113-C117 10m-73m Surcharge Sand upto +11.5mPD 15,210m3 5,000m3/day	3	27-Nov-15 A	20-Dec-15 A					
SUEC2a-1120	PC2a C113-C117 10m-73m Surcharge Sand Period 5mths (18May2016)	150	21-Dec-15	18-May-16	-177				
73-120m		240	14-Nov-15 A	10-Jul-16	-230				
SUEC2a-2090	PC2a C113-C117 73m-120m Surcharge Sand Period 8mths (10Jul2016)	240	14-Nov-15 A	10-Jul-16	-230				
Reclamation Areas		275	20-Sep-15 A	20-Jun-16	-630				
C2aC1		240	25-Oct-15 A	20-Jun-16	-630				
SURC2aC1-070	PC2a C2aC1 Sand Surcharge Period 8mths (20Jun2016)	240	25-Oct-15 A	20-Jun-16	-630				
C2aC2		241	20-Sep-15 A	17-May-16	-606				
SURC2aC2-070	PC2a C2aC2 Sand Surcharge Period 8mths (17May2016)	241	20-Sep-15 A	17-May-16	-606				

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016		
						Dec	Jan	Feb	Mar	
						49	50	51	52	
Land Portion C1a						243	21-Jul-15 A	19-Mar-16	-74	
Reclamation Areas						243	21-Jul-15 A	19-Mar-16	-74	
C3						119	15-Sep-15 A	11-Jan-16	-6	
SURC1a-030	PC1a Main Area East Sand Surcharge Removal 280,000m3 10,000m3/day	71	15-Sep-15 A	09-Dec-15 A						
SURC1a-040	PC1a Main Area West Sand Surcharge Removal 297,616m3 10,000m3/day	30	10-Dec-15 A	11-Jan-16	-5					
SURC1a-050	Completion of Section C1aC3	0		11-Jan-16	-6					
C4						243	21-Jul-15 A	19-Mar-16	-545	
SURC1a-140	PC1a South East Land Area Sand Surcharge Period at +11.5mPD 7mths (15Feb2016)	210	21-Jul-15 A	15-Feb-16	-516					
SURC1a-150	PC1a South West Land Area Sand Surcharge Period at +11.5mPD 8mths (16Mar2016)	240	21-Jul-15 A	16-Mar-16	-546					
SURC1a-160	PC1a South East Land Area Sand Surcharge Removal	3	16-Feb-16	18-Feb-16	-471					
SURC1a-170	PC1a South West Land Area Sand Surcharge Removal	3	17-Mar-16	19-Mar-16	-499					
SURC1a-180	Completion of Section C1aC4	0		19-Mar-16	-545					
Land Portion C1b						226	16-Aug-15 A	28-Mar-16	752	
Reclamation Areas						226	16-Aug-15 A	28-Mar-16	752	
West (1/4 Areas)						97	15-Sep-15 A	21-Dec-15	851	
SURC1b-024	PC1b West Instruction of Surcharge Removal stg2 by the Engioneer (Assumption)	0	21-Dec-15		851					
SURC1b-030	PC1b West Sand Surcharge Removal 336,434m310,000m3/day	71	15-Sep-15 A	06-Dec-15 A						
East (3/4 Areas)						37	07-Dec-15 A	31-Dec-15	840	
SURC1b-055	PC1b East Instruction of Surcharge Removal by the Engioneer (Assumption)	0	21-Dec-15*		851					
SURC1b-060	PC1b East Sand Surcharge Removal 336,435m3 10,000m3/day	34	07-Dec-15 A	31-Dec-15	-156					
SURC1b-095	Completion of Section PC1b	0		31-Dec-15	-92					
North Side close to Portion C2b						215	16-Aug-15 A	17-Mar-16	-245	
SURC1b-1030	PC1b Main Area Sand Surcharge Period as +11.5mPD 7mths (12Mar2016)	210	16-Aug-15 A	12-Mar-16	-244					

- Remaining Level of Effort
- Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- ▼ Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016					
						Dec		Jan		Feb		Mar			
						49	50	51	52						
SURC1b-1040	PC1b Main Area Sand Surcharge Removal 40,000m3 10,000m3/day	4	14-Mar-16	17-Mar-16	-224										
SURC1b-1050	Completion of Section PC1b North East at Reclamation Area close to C2b	0		17-Mar-16	-245										
North Side close to Portion C2c		210	01-Sep-15 A	28-Mar-16	-187										
SURC1b-1080	PC1b Main Area Sand Surcharge Period as +11.5mPD 7mths (28Mar2016)	210	01-Sep-15 A	28-Mar-16	-187										
Land Portion E2		362	16-Aug-15 A	11-Aug-16	-78										
North Part		254	20-Nov-15 A	30-Jul-16	-66										
Edge Areas - North, Land Area & Edge Area C064-C067		148	01-Jan-16	27-May-16	-294										
SUEE2-120	PE2 North & East Edge C064-C067 Sand Surcharge Laying up to 8.5mPD 54,746m3 5,000m3/day	11	01-Jan-16*	13-Jan-16	-252										
SUEE2-130	PE2 North & East Edge C064-C067 Sand Surcharge Period as +8.5mPD 4.5mths	135	14-Jan-16	27-May-16	-294										
Land Areas - East (TM) C057 - C063 Ch2+300 to Ch2+600		12	01-Jan-16	12-Jan-16	-341										
SURE2-055	PE2 Land C057-C063 Removal of Surcharge instructed by the Engineer	0	01-Jan-16*		-340										
SURE2-060	PE2 Land C057-C063 Tunnel Sand Surcharge Removal at tunnel area 107,437m3 10,000m3/day	11	01-Jan-16	12-Jan-16	-312										
Land Areas - West (C3)		254	20-Nov-15 A	30-Jul-16	-66										
SURE2-170-50	PE2 Land C061-C064 Non-Tunnel Sand Surcharge non tunnel area Laying upto 11.5mPD stg2 60,000m3 5,000m3/day	13	20-Nov-15 A	02-Jan-16	-57										
SURE2-180	PE2 Land C061-C064 Non-Tunnel Sand Surcharge Period as +11.5mPD non tunnel area 7mths	210	03-Jan-16	30-Jul-16	-66										
South Part		362	16-Aug-15 A	11-Aug-16	-206										
Edge Areas East C058 to C063		245	13-Oct-15 A	13-Jun-16	-505										
SUEE2-025	PE2 Edge C058-C063 Sand Surcharge Strength Test	49	13-Oct-15 A	31-Dec-15	-505										
SUEE2-030	PE2 Edge C058-C063 Sand Surcharge Laying up to +11.5mPD 70,806m3 5,000m3/day	13	01-Jan-16	15-Jan-16	-430										
SUEE2-040	PE2 Edge C058-C063 Sand Surcharge Period as +11.5mPD 5mths	150	16-Jan-16	13-Jun-16	-505										
Edge Areas East C056 to C057		272	11-Nov-15 A	08-Aug-16	-554										
SUEE2-630	PE2 Edge C056-C057 DCM Installation (229nrs , 12nos/day)	28	11-Nov-15 A	08-Dec-15 A											
SUEE2-640	PE2 Edge C056-C057 DCM Harden	30	09-Dec-15 A	07-Jan-16	-554										

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016						
						Dec		Jan		Feb		Mar				
						49	50	51	52	53	54	55	56			
SUEE2-650	PE2 Edge C056-C057 DCM Fill upto +5.5mPD	4	01-Jan-16*	04-Jan-16	-551											
SUEE2-660	PE2 Edge C056-C057 Remaining Area Fill upto +11.5mPD	4	08-Jan-16	11-Jan-16	-554											
SUEE2-670	PE2 Edge C056-C057 Remaining Area Surcharge Period 7mths	210	12-Jan-16	08-Aug-16	-554											
Edge Areas East C052 to C055		301	16-Oct-15 A	11-Aug-16	-558											
SURE2-420	PE2 Edge C052-C055 300m Zone Sand Surcharge Pause Period at 8.5mPD 4.5mths (27Feb2016)	135	16-Oct-15 A	27-Feb-16	-557											
SURE2-425	PE2 Edge C052-C055 300m Zone Sand Surcharge CPT Test at 8.5mPD	7	28-Feb-16	05-Mar-16	-557											
SURE2-430	PE2 Edge C052-C055 300m Zone Sand Surcharge Laying upto 11.5mPD 58,348m3 5,000m3/day	7	07-Mar-16	14-Mar-16	-475											
SURE2-440	PE2 Edge C052-C055 300m Zone Sand Surcharge Period as +11.5mPD 5mths	150	15-Mar-16	11-Aug-16	-558											
Land Areas		247	16-Aug-15 A	18-Apr-16	-91											
300m to 100m Zone		210	22-Sep-15 A	18-Apr-16	-449											
SURE2-530	PE2 Land C052-C056 300m Zone Sand Surcharge Period as +11.5mPD 7mths (18Apr2016)	210	22-Sep-15 A	18-Apr-16	-449											
Out of K052 300m		228	16-Aug-15 A	30-Mar-16	-72											
SURE2-020	PE2 Land C052-C060 Non-Tunnel Sand Surcharge Period as +11.5mPD 7mths (13Mar2016)	211	16-Aug-15 A	13-Mar-16	-72											
SURE2-030	PE2 Land C052-C060 Non-Tunnel Sand Surcharge Removal 158,673m3 + 28,116m3(C1b) 10,000m3/day	16	14-Mar-16	30-Mar-16	-63											
Land Portion E1		206	01-Dec-15 A	23-Jun-16	-661											
Deep Cement Mixing C077 - C080 150m (Exclude VB & RS)		206	01-Dec-15 A	23-Jun-16	-661											
DCM-4010	PE1 Edge Area Mobilization	7	01-Dec-15 A	07-Dec-15 A												
DCM-4020	PE1 Edge Area Installation 415nrs	42	08-Dec-15 A	09-Jan-16	-660											
DCM-4050	PE1 Edge Area Hardening	28	10-Jan-16	06-Feb-16	-660											
DCM-4060	PE1 Edge Area Filling upto +5.5mPD 25,000m3 5,000m3/day at DCM	6	25-Jan-16	30-Jan-16	-558											
DCM-4080	PE1 Edge Area Surcharge Filling up to +8.5mPD (10,000m3) 10,000m3/day at DCM	2	08-Feb-16	09-Feb-16	-564											
DCM-4083	PE1 Edge Area Surcharge Pause Period 4.5mths	135	10-Feb-16	23-Jun-16	-661											
Edge Areas Excluded 150m of DCM Area		162	05-Dec-15 A	14-May-16	-645											

- Remaining Level of Effort ◆ ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
SUEE1-005	PE1 Edge +5.5mPD Strength Test	14	05-Dec-15 A	13-Dec-15 A																	
SUEE1-010	PE1 Edge Sand Surcharge Laying up to 8.5mPD 126,529m3 10,000m3/day	13	14-Dec-15 A	31-Dec-15	-552																
SUEE1-020	PE1 Edge Sand Surcharge Period +8.5mPD 4.5mths	135	01-Jan-16	14-May-16	-645																
Land Portion C2b		260	12-Sep-15 A	28-May-16	-146																
Edge Areas		181	16-Nov-15 A	14-May-16	-212																
SUEC2b-050	PC2b Edge Area PBF Surcharge w compaction upto 8.5mPD 12,054m3 5,000m3/day	14	16-Nov-15 A	31-Dec-15	-197																
SUEC2b-060	PC2b Edge Area Surcharge Period as +8.5mPD 4.5mths	135	01-Jan-16	14-May-16	-212																
Reclamation Areas		260	12-Sep-15 A	28-May-16	-146																
North		210	01-Nov-15 A	28-May-16	-146																
SURC2b-020	PC2b Main Area North Sand Surcharge Period as +11.5mPD 7mths (28May2016)	210	01-Nov-15 A	28-May-16	-146																
South		211	12-Sep-15 A	09-Apr-16	-117																
SURC2b-034	PC2b Main Area South PBF Surcharge Period as +11.5mPD 7mths (9Apr2016)	211	12-Sep-15 A	09-Apr-16	-117																
Land Portion C2c		252	27-Oct-15 A	28-Jul-16	-122																
Edge Areas		144	01-Jan-16	23-May-16	-201																
SUEC2c-010	PC2c Edge Area PBF Surcharge w compaction upto 8.5mPD 43,395m3 5,000m3/day	9	01-Jan-16*	09-Jan-16	-187																
SUEC2c-020	PC2c Edge Area PBF Surcharge Period +8.5mPD 4.5mths	135	10-Jan-16	23-May-16	-201																
Reclamation Areas		252	27-Oct-15 A	28-Jul-16	-122																
West		210	27-Oct-15 A	14-May-16	-47																
SURC2c-W030	PC2c Main Area Sand Surcharge Period 7mths (23May2016)	210	27-Oct-15 A	14-May-16	-47																
East		252	20-Nov-15 A	28-Jul-16	-122																
SURC2c-E020	PC2c Main Area Sand Surcharge Laying upto 11.5mPD stg2 109,120m3 5,000m3/day	22	20-Nov-15 A	31-Dec-15	-105																
SURC2c-E030	PC2c Main Area Sand Surcharge Period 7mths	210	01-Jan-16	28-Jul-16	-122																
Geotechnical Instrumentation Works		43	17-Nov-15 A	20-Dec-15 A																	

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
Geotechnical Instrumentation Works for Seawalls																					
Cluster Type SD 26nrs Instrumentation and CPT Cluster behind cells																					
Portion E1																					
SD-13 C071																					
CTSD-130	Installation of SD-13 (C071) PE1	14	05-Dec-15 A	20-Dec-15 A																	
SD-14 C074																					
CTSD-140	Installation of SD-14 (C074) PE1	14	05-Dec-15 A	20-Dec-15 A																	
SD-15 C078																					
CTSD-150	Installation of SD-15 (C078) PE1	14	05-Dec-15 A	20-Dec-15 A																	
SD-16 C084																					
CTSD-160	Installation of SD-16 (C084) PE1	14	05-Dec-15 A	20-Dec-15 A																	
SD-17 C089																					
CTSD-170	Installation of SD-17 (C089) PE1	14	05-Dec-15 A	20-Dec-15 A																	
Geotechnical Instrumentation Works for Reclamation RA & RB																					
Settlement Marker Type 2																					
SMT2-100	M2 - Installation of Settlement Marker Type2 at PE1	14	17-Nov-15 A	20-Dec-15 A																	
Portion D																					
Precast Yard for Seawall Blocks & Culverts																					
Concrete Blocks																					
PD-PY1-0200	Precast Seawall Blocks for Permanent construction 1,990nrs (3,180 - 1190)	153	01-Aug-15 A	25-Dec-15	-498																
Culverts																					
Culverts EC1																					
EC1-5																					

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
- ▼ Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
PY-EC1-05060	PD EC1-05 Base Curing	16	13-Nov-15 A	28-Nov-15 A																	
EC1-6		15	21-Nov-15 A	05-Dec-15 A																	
PY-EC1-06050	PD EC1-06 Base Removal of Formwork	2	27-Nov-15 A	28-Nov-15 A																	
PY-EC1-06060	PD EC1-06 Base Curing	15	21-Nov-15 A	05-Dec-15 A																	
EC1-7		36	10-Nov-15 A	15-Dec-15 A																	
PY-EC1-07020	PD EC1-07 Base Reinforcement	14	10-Nov-15 A	23-Nov-15 A																	
PY-EC1-07030	PD EC1-07 Base Formwork	5	24-Nov-15 A	28-Nov-15 A																	
PY-EC1-07040	PD EC1-07 Base Concrete	2	29-Nov-15 A	30-Nov-15 A																	
PY-EC1-07050	PD EC1-07 Base Removal of Formwork	2	08-Dec-15 A	09-Dec-15 A																	
PY-EC1-07060	PD EC1-07 Base Curing	15	01-Dec-15 A	15-Dec-15 A																	
EC1-8		35	21-Nov-15 A	25-Dec-15	-498																
PY-EC1-08010	PD EC1-08 Casting Bed	4	21-Nov-15 A	24-Nov-15 A																	
PY-EC1-08020	PD EC1-08 Base Reinforcement	7	25-Nov-15 A	01-Dec-15 A																	
PY-EC1-08030	PD EC1-08 Base Formwork	7	02-Dec-15 A	08-Dec-15 A																	
PY-EC1-08040	PD EC1-08 Base Concrete	2	09-Dec-15 A	10-Dec-15 A																	
PY-EC1-08050	PD EC1-08 Base Removal of Formwork	2	18-Dec-15 A	19-Dec-15 A																	
PY-EC1-08060	PD EC1-08 Base Curing	15	11-Dec-15 A	25-Dec-15	-498																
Site Construction		187	15-Oct-15 A	16-Apr-16	733																
C1 to C4		187	15-Oct-15 A	16-Apr-16	733																
Installations of Precast Culverts except sloping outfalls		145	17-Nov-15 A	05-Mar-16	775																
Culvert C1		50	29-Nov-15 A	17-Jan-16	-208																
C1-2		12	21-Dec-15	01-Jan-16	-208																
PD-C1-2-060	PD C1-2 Removal of South Steel Bulkhead	4	21-Dec-15	24-Dec-15	-208																

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
PD-C1-2-070	PD C1-2 Manhole Insitu concrete	4	25-Dec-15	28-Dec-15	-208																
PD-C1-2-120	PD C1-2 Backfill Manhole upto +5.5mPD	4	29-Dec-15*	01-Jan-16	-208																
C1-3		37	30-Nov-15 A	05-Jan-16	-208																
PD-C1-3-090	PD C1-2/3 Movement Joint Insitu	4	30-Nov-15 A	03-Dec-15 A																	
PD-C1-3-120	PD C1-3 Backfill Manhole upto +5.5mPD	4	02-Jan-16	05-Jan-16	-208																
C1-4		4	06-Jan-16	09-Jan-16	-208																
PD-C1-4-120	PD C1-4 Backfill Manhole upto +5.5mPD	4	06-Jan-16	09-Jan-16	-208																
C1-5		46	29-Nov-15 A	13-Jan-16	-208																
PD-C1-5-070	PD C1-5 Manhole Insitu concrete	4	29-Nov-15 A	02-Dec-15 A																	
PD-C1-5-090	PD C1-4/5 Movement Joint Insitu	4	01-Dec-15 A	04-Dec-15 A																	
PD-C1-5-120	PD C1-5 Backfill Manhole upto +5.5mPD	4	10-Jan-16	13-Jan-16	-208																
C1-6		28	21-Dec-15	17-Jan-16	-208																
PD-C1-6-050	PD C1-6 Removal of North Steel Bulkhead	4	21-Dec-15	24-Dec-15	-413																
PD-C1-6-070	PD C1-6 Manhole Insitu concrete	4	21-Dec-15	24-Dec-15	-188																
PD-C1-6-090	PD C1-5/6 Movement Joint Insitu	4	21-Dec-15	24-Dec-15	-188																
PD-C1-6-120	PD C1-6 Backfill Manhole upto +5.5mPD	4	14-Jan-16	17-Jan-16	-208																
Culvert C2		78	17-Nov-15 A	02-Feb-16	807																
C2-2		34	19-Dec-15 A	21-Jan-16	819																
PD-C2-2-060	PD C2-2 Removal of South Steel Bulkhead	4	21-Dec-15	24-Dec-15	847																
PD-C2-2-070	PD C2-2 Manhole Insitu concrete	4	19-Dec-15 A	23-Dec-15	-183																
PD-C2-2-120	PD C2-2 Backfill Manhole upto +5.5mPD	4	18-Jan-16	21-Jan-16	-208																
C2-3		4	22-Jan-16	25-Jan-16	-208																
PD-C2-3-120	PD C2-3 Backfill Manhole upto +5.5mPD	4	22-Jan-16	25-Jan-16	-208																

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

Page 14 of 25

TASK filters: No Option 1 2, Three Month Rolling.

Primavera Systems, Inc.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016			
						Dec		Jan		Feb		Mar	
						49	50	51	52	53	54	55	56
C2-4		65	26-Nov-15 A	29-Jan-16	-208								
PD-C2-4-070	PD C2-4 Manhole Insitu concrete	4	26-Nov-15 A	30-Nov-15 A									
PD-C2-4-120	PD C2-4 Backfill Manhole upto +5.5mPD	4	26-Jan-16	29-Jan-16	-208								
C2-5		78	17-Nov-15 A	02-Feb-16	807								
PD-C2-5-050	PD C2-5 Removal of North Steel Bulkhead	4	21-Dec-15	24-Dec-15	847								
PD-C2-5-070	PD C2-5 Manhole Insitu concrete	4	11-Dec-15 A	15-Dec-15 A									
PD-C2-5-090	PD C2-4/5 Movement Joint Insitu	6	17-Nov-15 A	22-Nov-15 A									
PD-C2-5-120	PD C2-5 Backfill Manhole upto +5.5mPD	4	30-Jan-16	02-Feb-16	-208								
Culvert C3		129	19-Nov-15 A	18-Feb-16	791								
C3-2		50	19-Dec-15 A	06-Feb-16	803								
PD-C3-2-060	PD C3-2 Removal of South Steel Bulkhead	4	21-Dec-15	24-Dec-15	847								
PD-C3-2-070	PD C3-2 Manhole Insitu concrete	4	19-Dec-15 A	24-Dec-15	-168								
PD-C3-2-120	PD C3-2 Backfill Manhole upto +5.5mPD	4	03-Feb-16	06-Feb-16	-208								
C3-3		84	19-Nov-15 A	10-Feb-16	-208								
PD-C3-3-070	PD C3-3 Manhole Insitu concrete	4	22-Nov-15 A	26-Nov-15 A									
PD-C3-3-090	PD C3-2/3 Movement Joint Insitu	4	19-Nov-15 A	22-Nov-15 A									
PD-C3-3-120	PD C3-3 Backfill Manhole upto +5.5mPD	4	07-Feb-16	10-Feb-16	-208								
C3-4		125	19-Nov-15 A	14-Feb-16	-208								
PD-C3-4-070	PD C3-4 Manhole Insitu concrete	4	30-Nov-15 A	04-Dec-15 A									
PD-C3-4-090	PD C3-3/4 Movement Joint Insitu	4	19-Nov-15 A	23-Nov-15 A									
PD-C3-4-120	PD C3-4 Backfill Manhole upto +5.5mPD	4	11-Feb-16	14-Feb-16	-208								
C3-5		80	01-Dec-15 A	18-Feb-16	-192								
PD-C3-5-050	PD C3-5 Removal of North Steel Bulkhead	4	21-Dec-15	24-Dec-15	-509								

- Remaining Level of Effort ◆ ◆ Milestone
- Actual Level of Effort ◆ ◆ Milestone
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-C3-5-070	PD C3-5 Manhole Insitu concrete	4	21-Dec-15	24-Dec-15	-156				
PD-C3-5-090	PD C3-4/5 Movement Joint Insitu	4	01-Dec-15 A	04-Dec-15 A					
PD-C3-5-120	PD C3-5 Backfill Manhole upto +5.5mPD	4	15-Feb-16	18-Feb-16	-208				
PD-C3-5-130	PD C3 Handover to Hy/2013/02	0		21-Dec-15	-132				
Culvert C4		109	21-Nov-15 A	05-Mar-16	775				
C4-2		94	21-Nov-15 A	22-Feb-16	787				
PD-C4-2-050	PD C4-2 Removal of North Steel Bulkhead	3	21-Nov-15 A	23-Nov-15 A					
PD-C4-2-060	PD C4-2 Removal of South Steel Bulkhead	4	25-Dec-15	28-Dec-15	843				
PD-C4-2-070	PD C4-2 Manhole Insitu concrete	4	15-Dec-15 A	19-Dec-15 A					
PD-C4-2-120	PD C4-2 Backfill Manhole upto +5.5mPD	4	19-Feb-16	22-Feb-16	-208				
C4-3		81	08-Dec-15 A	26-Feb-16	-208				
PD-C4-3-070	PD C4-3 Manhole Insitu concrete	4	08-Dec-15 A	12-Dec-15 A					
PD-C4-3-080	PD C4-2/3 Movement Joint Installation	2	08-Dec-15 A	12-Dec-15 A					
PD-C4-3-090	PD C4-2/3 Movement Joint Insitu	4	09-Dec-15 A	12-Dec-15 A					
PD-C4-3-120	PD C4-3 Backfill Manhole upto +5.5mPD	4	23-Feb-16	26-Feb-16	-208				
C4-4		105	25-Nov-15 A	01-Mar-16	-208				
PD-C4-4-060	PD C4-4 Removal of South Steel Bulkhead	4	25-Nov-15 A	28-Nov-15 A					
PD-C4-4-070	PD C4-4 Manhole Insitu concrete	4	13-Dec-15 A	17-Dec-15 A					
PD-C4-4-080	PD C4-3/4 Movement Joint Installation	2	18-Dec-15 A	19-Dec-15 A					
PD-C4-4-090	PD C4-3/4 Movement Joint Insitu	4	09-Dec-15 A	12-Dec-15 A					
PD-C4-4-110	PD C4-4 Backfill upto +3.5mPD except Manholes	7	03-Dec-15 A	05-Dec-15 A					
PD-C4-4-120	PD C4-4 Backfill Manhole upto +5.5mPD	4	27-Feb-16	01-Mar-16	-208				
C4-5		98	29-Nov-15 A	05-Mar-16	-208				

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-C4-5-050	PD C4-5 Removal of North Steel Bulkhead	3	21-Dec-15	23-Dec-15	-438				
PD-C4-5-060	PD C4-5 Removal of South Steel Bulkhead	4	29-Nov-15 A	03-Dec-15 A					
PD-C4-5-070	PD C4-5 Manhole Insitu concrete	4	21-Dec-15	24-Dec-15	-140				
PD-C4-5-080	PD C4-4/5 Movement Joint Installation	2	21-Dec-15	22-Dec-15	-142				
PD-C4-5-090	PD C4-4/5 Movement Joint Insitu	4	23-Dec-15	26-Dec-15	-142				
PD-C4-5-100	PD C4-5 Backfill Beside of Culvert	2	03-Dec-15 A	05-Dec-15 A					
PD-C4-5-110	PD C4-5 Backfill upto +3.5mPD except Manholes	3	06-Dec-15 A	07-Dec-15 A					
PD-C4-5-120	PD C4-5 Backfill Manhole upto +5.5mPD	4	02-Mar-16	05-Mar-16*	-208				
PD-C4-5-130	PD C4 Handover to Hy/2013/02	0		21-Dec-15	-132				
Permanent Access to Portion A		56	21-Dec-15	14-Feb-16	795				
PD-A2090	PD - C2 Divert Access	21	04-Jan-16*	24-Jan-16	-463				
PD-A2100	PD - C3 Divert Access	21	25-Jan-16	14-Feb-16	-463				
PD-A2110	PD - C4 Divert Access	21	21-Dec-15	10-Jan-16	-403				
PD-A2140	Completion of Access to PA	0		14-Feb-16	795				
Removal of Temporary Access to Portion A		35	25-Jan-16	28-Feb-16	-445				
PD-A1110	PD C2 - Removal of Temporary Access	7	25-Jan-16	31-Jan-16	-463				
PD-A1120	PD C3 - Removal of Temporary Access	7	15-Feb-16	21-Feb-16	-463				
PD-A1130	PD C4 - Removal of Temporary Access	7	22-Feb-16	28-Feb-16	-445				
Construction of Sloping Outfalls		123	19-Nov-15 A	20-Mar-16	-445				
Culvert C1 Sloping Outfall		69	19-Nov-15 A	26-Jan-16	-418				
PD-C1-0110	PD C1-1 Outfall Excavation	24	19-Nov-15 A	12-Dec-15 A					
PD-C1-0120	PD C1-1 Outfall Formation	7	13-Dec-15 A	19-Dec-15 A					
PD-C1-0125	PD C1-1 Buoyancy	2	30-Dec-15	31-Dec-15	-504				

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-C1-0130	PD C1-1 Outfall Installation	1	01-Jan-16	01-Jan-16	-504				
PD-C1-0140	PD C1-1 Outfall Removal of Buoyancy & Bulkhead	4	02-Jan-16	05-Jan-16	-418				
PD-C1-0150	PD C1-1 Outfall Insitu Concrete	14	06-Jan-16	19-Jan-16	-418				
PD-C1-0160	PD C1-1 Outfall Backfill	7	20-Jan-16	26-Jan-16	-418				
Culvert C2 Sloping Outfall		67	12-Jan-16	18-Mar-16	-463				
PD-C2-0110	PD C2-1 Outfall Excavation	14	01-Feb-16	14-Feb-16	-463				
PD-C2-0120	PD C2-1 Outfall Formation	7	15-Feb-16	21-Feb-16	-463				
PD-C2-0125	PD C2-1 Buoyancy	2	12-Jan-16	13-Jan-16	-424				
PD-C2-0130	PD C2-1 Outfall Installation	1	22-Feb-16	22-Feb-16	-463				
PD-C2-0140	PD C2-1 Outfall Removal of Buoyancy & Bulkhead	4	23-Feb-16	26-Feb-16	-463				
PD-C2-0150	PD C2-1 Outfall Insitu Concrete	14	27-Feb-16	11-Mar-16	-463				
PD-C2-0160	PD C2-1 Outfall Backfill	7	12-Mar-16	18-Mar-16	-463				
Culvert C3 Sloping Outfall		28	22-Feb-16	20-Mar-16	-463				
PD-C3-0110	PD C3-1 Outfall Excavation	14	22-Feb-16	06-Mar-16	-463				
PD-C3-0120	PD C3-1 Outfall Formation	7	07-Mar-16	13-Mar-16	-463				
PD-C3-0122	PD C3-1 & C4-1 Back & Delivery Stg18	7	23-Feb-16	29-Feb-16	-452				
PD-C3-0125	PD C3-1 Buoyancy	2	01-Mar-16	02-Mar-16	-452				
PD-C3-0130	PD C3-1 Outfall Installation	3	14-Mar-16	16-Mar-16	-463				
PD-C3-0140	PD C3-1 Outfall Removal of Buoyancy & Bulkhead	4	17-Mar-16	20-Mar-16	-463				
Culvert C4 Sloping Outfall		14	07-Mar-16	20-Mar-16	-445				
PD-C4-0110	PD C4-1 Outfall Excavation	14	07-Mar-16	20-Mar-16	-452				
PD-C4-0125	PD C4-1 Buoyancy	2	15-Mar-16	16-Mar-16	-441				
Extension Culvert EC1 by one submerble barge		158	20-Oct-15 A	25-Mar-16	755				

— Remaining Level of Effort ◆ Milestone
— Actual Level of Effort ▼ Summary
— Actual Work
— Remaining Work
— Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

Page 18 of 25

TASK filters: No Option 1 2, Three Month Rolling.

Primavera Systems, Inc.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016			
						Dec	Jan	Feb	Mar		
						49	50	51	52		
Excavation & Supporting						53	20-Oct-15 A	11-Jan-16	829		
PD-EC1-0-020	PD EC1 Excavation 31,000m3	50	20-Oct-15 A	11-Jan-16	801						
PD-EC1-0-050	PD EC1 Formation of Foundation EC1-7 & EC1-8	7	20-Nov-15 A	26-Dec-15	845						
Insitu Concrete						129	18-Nov-15 A	25-Mar-16	755		
EC1-1						84	18-Nov-15 A	09-Feb-16	800		
PD-EC1-1-010	PD EC1-1, EC1-2 & EC1-3 Back & Delivery stg14	11	18-Nov-15 A	28-Dec-15	843						
PD-EC1-1-020	PD EC1-1 Buoyancy	2	26-Nov-15 A	27-Nov-15 A							
PD-EC1-1-030	PD EC1-1 Installation of Precast Culvert Base	1	28-Nov-15 A	30-Nov-15 A							
PD-EC1-1-040	PD EC1-1 Removal of Buoyancy	2	01-Dec-15 A	02-Dec-15 A							
PD-EC1-1-050	PD EC1-1 Wall Insitu Concrete	12	21-Dec-15	02-Jan-16	-487						
PD-EC1-1-060	PD EC1-1 Wall Curing	7	03-Jan-16	09-Jan-16	-381						
PD-EC1-1-070	PD EC1-1 Removal of Extenal Wall Fomwork	4	10-Jan-16	13-Jan-16	-381						
PD-EC1-1-080	PD EC1-1 Base insitu Concrete	7	03-Jan-16	09-Jan-16	-478						
PD-EC1-1-090	PD EC1-1 Top Slab Insitu Concrete	12	11-Jan-16	22-Jan-16	-478						
PD-EC1-1-100	PD EC1-1 Top Slab Curing	14	23-Jan-16	05-Feb-16	-519						
PD-EC1-1-110	PD EC1-1 Removal of Internal Wall Fomwork	4	06-Feb-16	09-Feb-16	-519						
EC1-2						78	28-Nov-15 A	13-Feb-16	-406		
PD-EC1-2-020	PD EC1-2 Buoyancy	2	28-Nov-15 A	30-Nov-15 A							
PD-EC1-2-030	PD EC1-2 Installation of Precast Culvert Base	1	03-Dec-15 A	04-Dec-15 A							
PD-EC1-2-040	PD EC1-2 Removal of Buoyancy	2	05-Dec-15 A	06-Dec-15 A							
PD-EC1-2-050	PD EC1-2 Wall Insitu Concrete	12	17-Dec-15 A	02-Jan-16	-479						
PD-EC1-2-060	PD EC1-2 Wall Curing	7	03-Jan-16	09-Jan-16	-375						
PD-EC1-2-070	PD EC1-2 Removal of Extenal Wall Fomwork	4	10-Jan-16	13-Jan-16	-375						

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-EC1-2-080	PD EC1-2 Base insitu Concrete	7	03-Jan-16	09-Jan-16	-475				
PD-EC1-2-090	PD EC1-2 Top Slab Insitu Concrete	12	11-Jan-16	22-Jan-16	-475				
PD-EC1-2-100	PD EC1-2 Top Slab Curing	14	23-Jan-16	05-Feb-16	-515				
PD-EC1-2-110	PD EC1-2 Removal of Internal Wall Fomwork	4	10-Feb-16	13-Feb-16	-519				
EC1-3		84	01-Dec-15 A	22-Feb-16	-409				
PD-EC1-3-020	PD EC1-3 Buoyancy	2	01-Dec-15 A	03-Dec-15 A					
PD-EC1-3-030	PD EC1-3 Installation of Precast Culvert Base	1	05-Dec-15 A	05-Dec-15 A					
PD-EC1-3-040	PD EC1-3 Removal of Buoyancy	2	06-Dec-15 A	07-Dec-15 A					
PD-EC1-3-050	PD EC1-3 Wall Insitu Concrete	12	03-Jan-16	15-Jan-16	-487				
PD-EC1-3-060	PD EC1-3 Wall Curing	7	16-Jan-16	22-Jan-16	-382				
PD-EC1-3-070	PD EC1-3 Removal of Extenal Wall Fomwork	4	23-Jan-16	26-Jan-16	-382				
PD-EC1-3-080	PD EC1-3 Base insitu Concrete	7	16-Jan-16	22-Jan-16	-483				
PD-EC1-3-090	PD EC1-3 Top Slab Insitu Concrete	12	23-Jan-16	04-Feb-16	-483				
PD-EC1-3-100	PD EC1-3 Top Slab Curing	14	05-Feb-16	18-Feb-16	-524				
PD-EC1-3-110	PD EC1-3 Removal of Internal Wall Fomwork	4	19-Feb-16	22-Feb-16	-524				
EC1-4		83	06-Dec-15 A	26-Feb-16	-406				
PD-EC1-4-010	PD EC1-4, EC1-5 & EC1-6 Back & Delivery stg15	9	06-Dec-15 A	12-Dec-15 A					
PD-EC1-4-020	PD EC1-4 Buoyancy	2	13-Dec-15 A	14-Dec-15 A					
PD-EC1-4-030	PD EC1-4 Installation of Precast Culvert Base	1	15-Dec-15 A	15-Dec-15 A					
PD-EC1-4-040	PD EC1-4 Removal of Buoyancy	2	16-Dec-15 A	17-Dec-15 A					
PD-EC1-4-050	PD EC1-4 Wall Insitu Concrete	12	03-Jan-16	15-Jan-16	-479				
PD-EC1-4-060	PD EC1-4 Wall Curing	7	16-Jan-16	22-Jan-16	-375				
PD-EC1-4-070	PD EC1-4 Removal of Extenal Wall Fomwork	4	23-Jan-16	26-Jan-16	-375				


- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-EC1-4-080	PD EC1-4 Base insitu Concrete	7	16-Jan-16	22-Jan-16	-479				
PD-EC1-4-090	PD EC1-4 Top Slab Insitu Concrete	12	23-Jan-16	04-Feb-16	-479				
PD-EC1-4-100	PD EC1-4 Top Slab Curing	14	05-Feb-16	18-Feb-16	-520				
PD-EC1-4-110	PD EC1-4 Removal of Internal Wall Fomwork	4	23-Feb-16	26-Feb-16	-524				
EC1-5		86	16-Dec-15 A	10-Mar-16	-413				
PD-EC1-5-020	PD EC1-5 Buoyancy	2	16-Dec-15 A	17-Dec-15 A					
PD-EC1-5-030	PD EC1-5 Installation of Precast Culvert Base	1	18-Dec-15 A	18-Dec-15 A					
PD-EC1-5-040	PD EC1-5 Removal of Buoyancy	2	19-Dec-15 A	20-Dec-15 A					
PD-EC1-5-050	PD EC1-5 Wall Insitu Concrete	12	16-Jan-16	28-Jan-16	-487				
PD-EC1-5-060	PD EC1-5 Wall Curing	7	29-Jan-16	04-Feb-16	-382				
PD-EC1-5-070	PD EC1-5 Removal of Extenal Wall Fomwork	4	05-Feb-16	08-Feb-16	-382				
PD-EC1-5-080	PD EC1-5 Base insitu Concrete	7	29-Jan-16	04-Feb-16	-487				
PD-EC1-5-090	PD EC1-5 Top Slab Insitu Concrete	12	05-Feb-16	21-Feb-16	-487				
PD-EC1-5-100	PD EC1-5 Top Slab Curing	14	22-Feb-16	06-Mar-16	-533				
PD-EC1-5-110	PD EC1-5 Removal of Internal Wall Fomwork	4	07-Mar-16	10-Mar-16	-533				
EC1-6		87	19-Dec-15 A	14-Mar-16	-410				
PD-EC1-6-020	PD EC1-6 Buoyancy	2	19-Dec-15 A	20-Dec-15 A					
PD-EC1-6-030	PD EC1-6 Installation of Precast Culvert Base	1	21-Dec-15	21-Dec-15	-504				
PD-EC1-6-040	PD EC1-6 Removal of Buoyancy	2	22-Dec-15	23-Dec-15	-499				
PD-EC1-6-050	PD EC1-6 Wall Insitu Concrete	12	16-Jan-16	28-Jan-16	-478				
PD-EC1-6-060	PD EC1-6 Wall Curing	7	29-Jan-16	04-Feb-16	-375				
PD-EC1-6-070	PD EC1-6 Removal of Extenal Wall Fomwork	4	05-Feb-16	08-Feb-16	-375				
PD-EC1-6-080	PD EC1-6 Base insitu Concrete	7	29-Jan-16	04-Feb-16	-473				

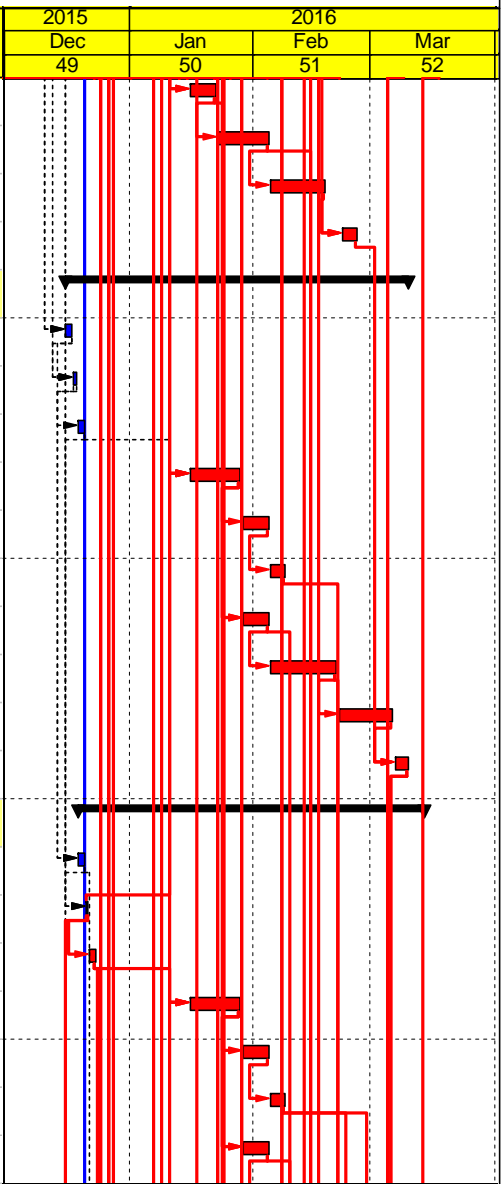

- Remaining Level of Effort ◆ Milestone
- Actual Level of Effort ▼ Summary
- Actual Work
- Remaining Work
- Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. Hong Kong - Zhuhai - Macao Bridge

Hong Kong Boundary Crossing Facilities - Reclamation Works

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-EC1-6-090	PD EC1-6 Top Slab Insitu Concrete	12	05-Feb-16	21-Feb-16	-465				
PD-EC1-6-100	PD EC1-6 Top Slab Curing	14	22-Feb-16	06-Mar-16	-509				
PD-EC1-6-110	PD EC1-6 Removal of Internal Wall Fomwork	4	11-Mar-16	14-Mar-16	-513				
EC1-7		94	21-Dec-15	23-Mar-16	-413				
PD-EC1-7-010	PD EC1-7 & C1-1 Back & Delivery stg16	6	21-Dec-15	26-Dec-15	-504				
PD-EC1-7-020	PD EC1-7 Buoyancy	2	27-Dec-15	28-Dec-15	-504				
PD-EC1-7-030	PD EC1-7 Installation of Precast Culvert Base	1	29-Dec-15	29-Dec-15	-504				
PD-EC1-7-040	PD EC1-7 Removal of Buoyancy	2	30-Dec-15	31-Dec-15	-497				
PD-EC1-7-050	PD EC1-7 Wall Insitu Concrete	12	29-Jan-16	13-Feb-16	-483				
PD-EC1-7-060	PD EC1-7 Wall Curing	7	14-Feb-16	20-Feb-16	-385				
PD-EC1-7-070	PD EC1-7 Removal of Extenal Wall Fomwork	4	21-Feb-16	24-Feb-16	-385				
PD-EC1-7-080	PD EC1-7 Base insitu Concrete	7	15-Feb-16	21-Feb-16	-483				
PD-EC1-7-090	PD EC1-7 Top Slab Insitu Concrete	12	22-Feb-16	05-Mar-16	-483				
PD-EC1-7-100	PD EC1-7 Top Slab Curing	14	06-Mar-16	19-Mar-16	-518				
PD-EC1-7-110	PD EC1-7 Removal of Internal Wall Fomwork	4	20-Mar-16	23-Mar-16	-518				
EC1-8		71	01-Jan-16	11-Mar-16	-394				
PD-EC1-8-010	PD EC1-8 & C2-1 Back & Delivery stg17	8	01-Jan-16	08-Jan-16	-504				
PD-EC1-8-020	PD EC1-8 Buoyancy	2	09-Jan-16	10-Jan-16	-504				
PD-EC1-8-030	PD EC1-8 Outfall Installation of Precast Culvert Base	1	11-Jan-16	11-Jan-16	-504				
PD-EC1-8-040	PD EC1-8 Removal of Buoyancy	2	12-Jan-16	13-Jan-16	-504				
PD-EC1-8-050	PD EC1-8 Outfall Wall Insitu Concrete	12	29-Jan-16	13-Feb-16	-478				
PD-EC1-8-060	PD EC1-8 Outfall Wall Curing	7	14-Feb-16	20-Feb-16	-378				
PD-EC1-8-070	PD EC1-8 Removal of Extenal Wall Fomwork	4	21-Feb-16	24-Feb-16	-378				

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Contract No. **Hong Kong - Zhuhai - Macao Bridge** **Hong Kong Boundary Crossing Facilities - Reclamation Works**

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015		2016	
						Dec	Jan	Feb	Mar
						49	50	51	52
PD-EC1-8-080	PD EC1-8 Outfall Base insitu Concrete	7	15-Feb-16	21-Feb-16	-478				
PD-EC1-8-090	PD EC1-8 Outfall Insitu Concrete	7	22-Feb-16	29-Feb-16	-478				
PD-EC1-8-100	PD EC1-8 Outfall Curing	7	01-Mar-16	07-Mar-16	-506				
PD-EC1-8-110	PD EC1-8 Removal of Internal Wall Fomwork	4	08-Mar-16	11-Mar-16	-506				
Connection to the Existing Culvert		14	11-Mar-16	25-Mar-16	-488				
PD-EC1-0-10	PD EC1-0 South Wall Insitu Concrete	14	11-Mar-16	25-Mar-16	-488				
Backfilling & Reclamation		70	14-Jan-16	23-Mar-16	-51				
PD-EC1-0100-020	PD EC1-1 Backfill and Compaction	6	28-Jan-16	02-Feb-16	-363				
PD-EC1-0100-030	PD EC1-2 Backfill and Compaction	6	03-Feb-16	12-Feb-16	-363				
PD-EC1-0100-040	PD EC1-3 Backfill and Compaction	6	13-Feb-16	19-Feb-16	-363				
PD-EC1-0100-050	PD EC1-4 Backfill and Compaction	6	20-Feb-16	25-Feb-16	-363				
PD-EC1-0100-060	PD EC1-5 Backfill and Compaction	6	27-Feb-16	04-Mar-16	-364				
PD-EC1-0100-070	PD EC1-6 Backfill and Compaction	6	05-Mar-16	10-Mar-16	-364				
PD-EC1-0100-080	PD EC1-7 Backfill and Compaction	6	11-Mar-16	17-Mar-16	-364				
PD-EC1-0100-090	PD EC1-8 Outfall Backfill and Compaction	6	18-Mar-16	23-Mar-16	-364				
PD-EC1-0100-100	Backfill west side of EC1-1 to EC1-6 for Handover to Other Contractors	36	14-Jan-16	18-Feb-16	-192				
PD-EC1-0100-110	Handover EC1 40m strip to other Contractor	0		19-Feb-16*	-18				
Construction of Permanent Seawall		168	15-Oct-15 A	16-Apr-16	-435				
Vertical Seawall Type V2 6+136 to 5+650		168	15-Oct-15 A	16-Apr-16	-463				
Foundation Leveling		107	15-Oct-15 A	06-Feb-16	-431				
PD-V2-0055	PD C1/C2 - Vertical Seawall V2 VSOP19-16 Foundation Leveling 3,000m2 and Geotextile	45	15-Oct-15 A	01-Jan-16	-476				
PD-V2-0060	PD C2/C3 - Vertical Seawall V2 VSOP15-11 Foundation Leveling 3,000m2 and Geotextile	14	02-Jan-16	16-Jan-16	-476				
PD-V2-0065	PD C3/C4 - Vertical Seawall V2 VSOP10-05 Foundation Leveling 3,000m2 and Geotextile	14	20-Nov-15 A	22-Jan-16	-455				

█ Remaining Level of Effort ◆ Milestone
█ Actual Level of Effort ▼ Summary
█ Actual Work
█ Remaining Work
█ Critical Remaining Work

49th_7 Monthly Progress Report Status as on 21Dec2015

Page 23 of 25

TASK filters: No Option 1 2, Three Month Rolling.

Primavera Systems, Inc.

Contract No. Hong Kong - Zhuhai - Macao Bridge Hong Kong Boundary Crossing Facilities - Reclamation Works








Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
PD-V2-920	PD C4 East - Vertical Seawall V2 VSOP04-01 Foundation Leveling 3,000m2 and Geotextile	14	23-Jan-16	06-Feb-16	-431																
Seawall Blocks Installation		117	14-Nov-15 A	22-Mar-16	-476	[Summary bar]															
PD-V2-0090	PD C1/C2 - Vertical Seawall Blocks V2 VSOP19-16 Type 2A5, 2A4 & 2A3 606nrs (30nrs/day)	21	14-Nov-15 A	14-Jan-16	-474																
PD-V2-0110	PD C2/C3 - Vertical Seawall Blocks V2 VSOP15-11 Type 2A x3 & 2D 808nrs (30nrs/day)	27	17-Jan-16	18-Feb-16	-476																
PD-V2-0130	PD C3/C4 - Vertical Seawall Blocks V2 VSOP10-05 Type 2A x4, 2AC 905nrs (30nrs/day)	31	19-Feb-16	22-Mar-16	-476																
Rockfill Type 2 behind seawall		36	15-Jan-16	25-Feb-16	-467	[Summary bar]															
PD-V2-0190	PD C1/C2 - Vertical Seawall V2 Rockf ill Type 2 VSOP19-16 2,100m3	4	15-Jan-16	18-Jan-16	-455																
PD-V2-0200	PD C2/C3 - Vertical Seawall V2 Rockf ill Type 2 VSOP15-11 3,400m3	7	19-Feb-16	25-Feb-16	-467																
Geotextile Type 1		37	19-Jan-16	02-Mar-16	-467	[Summary bar]															
PD-V2-0240	PD C1/C2 - Vertical Seawall V2 Geotextile Type 1 VSOP19-16 1,500m2	3	19-Jan-16	21-Jan-16	-455																
PD-V2-0250	PD C2/C3 - Vertical Seawall V2 Geotextile Type 1 VSOP15-11 2,400m2	5	26-Feb-16	02-Mar-16	-467																
Reclamation upto +3.25mPD		42	22-Jan-16	10-Mar-16	-467	[Summary bar]															
PD-V2-0290	PD C1/C2 - Vertical Seawall V2 backfill with compaction upto +3.25mPD VSOP20-16	8	22-Jan-16	30-Jan-16	-455																
PD-V2-0300	PD C2/C3 - Vertical Seawall V2 backfill with compaction upto +3.25mPD VSOP16-11	8	03-Mar-16	10-Mar-16	-467																
Insitu Concrete Coping		68	31-Jan-16	16-Apr-16	-467	[Summary bar]															
PD-V2-0340	PD C1/C2 - Vertical Seawall V2 Insitu Coping VSOP20-16 11bays	22	31-Jan-16	26-Feb-16	-455																
PD-V2-0350	PD C2/C3 - Vertical Seawall V2 Insitu Coping VSOP16-11 17bays	34	11-Mar-16	16-Apr-16	-467																
Reclamation upto +5.5mPD		12	27-Feb-16	10-Mar-16	-433	[Summary bar]															
PD-V2-0390	PD C1/2 - Vertical Seawall V2 backfill with compaction upto +5.5mPD VSOP20-16	12	27-Feb-16	10-Mar-16	-433																
Rock Armour		43	15-Jan-16	04-Mar-16	-423	[Summary bar]															
PD-V2-0920	PD C1/2 - Vertical Seawall V2 Armour VSOP20-16	14	15-Jan-16	29-Jan-16	-408																
PD-V2-0930	PD C2/3 - Vertical Seawall V2 Armour VSOP16-11	14	19-Feb-16	04-Mar-16	-423																
Sloping Seawall Type S1 0+000 to 0+420		14	19-Mar-16	02-Apr-16	-422	[Summary bar]															

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

49th_7 Monthly Progress Report Status as on 21Dec2015

TASK filters: No Option 1 2, Three Month Rolling.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2015				2016											
						Dec				Jan				Feb				Mar			
						49				50				51				52			
Removal of South Temporary Seawall S1																					
PD-S1-0015	PD C2 - Removal of S1 Temporary seawall West2 0+100 to 0+200	14	19-Mar-16	02-Apr-16	-422																
Works Area WA2 (Tung Chung)																					
Zone A																					
A1880	Maintenance of Engineer's Accommodation (28Feb2017)	1434	21-May-12 A	29-Mar-17	-25																
Works Area TKO Fill Bank																					
WA-TKO-1040	Operate and Maintain Public Fill Sorting Facilities in Zone A, B1 & B2 (30Nov2016)	1254	25-Sep-12 A	30-Dec-16	-25																

-  Remaining Level of Effort  Milestone
-  Actual Level of Effort  Summary
-  Actual Work
-  Remaining Work
-  Critical Remaining Work

Appendix C - Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
Air Quality				
S5.5.6.1 of HKBCFEIA	A1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	All construction sites	V
S5.5.6.2 of HKBCFEIA and S4.8.1 of TKCLKLEIA	A2	Proper watering of exposed spoil should be undertaken throughout the construction phase: <ul style="list-style-type: none"> • Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; • A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones. • Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;</p> <ul style="list-style-type: none"> • The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Any skip hoist for material transport should be totally enclosed by impervious sheeting; • Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; • Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;</p> <ul style="list-style-type: none"> • All unpaved roads/exposed area shall be watered which results in dust suppression by forming moist cohesive films among the discrete grains of road surface material. • No burning of debris or other materials on the works areas is allowed; • Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created; • Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading; • During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport. Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards; • Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and • Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.		
S5.5.6.3 of HKBCFEIA and S4.8.1 of TKCLKLEIA	A3	The Contractor should undertake proper watering on all exposed spoil and associated work areas (with at least 8 times per day) throughout the construction phase.	All construction sites	V
S5.5.6.4 of HKBCFEIA and S4.11 of TKCLKLEIA	A4	Implement regular dust monitoring under EM&A programme during the construction stage.	Selected representative dust monitoring station	V
S5.5.7.1 of HKBCFEIA	A5	The following mitigation measures should be adopted to prevent fugitive dust emissions for concrete batching plant: <ul style="list-style-type: none"> • Loading, unloading, handling, transfer or storage of any dusty materials should be carried out in totally enclosed system; • All dust-laden air or waste gas generated by the process operations should be properly extracted and vented to fabric filtering system to meet the emission limits for TSP; • Vents for all silos and cement/ pulverised fuel ash (PFA) weighing scale should be fitted with fabric filtering system; • The materials which may generate airborne dusty emissions should be wetted by water spray system; 	All construction sites	N/A

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • All receiving hoppers should be enclosed on three sides up to 3m above unloading point; • All conveyor transfer points should be totally enclosed; • All access and route roads within the premises should be paved and wetted; and • Vehicle cleaning facilities should be provided and used by all concrete trucks before leaving the premises to wash off any dust on the wheels and/or body. 		
S5.5.2.7 of HKBCFEIA	A6	The following mitigation measures should be adopted to prevent fugitive dust emissions at barging point: <ul style="list-style-type: none"> • All road surface within the barging facilities will be paved; • Dust enclosures will be provided for the loading ramp; • Vehicles will be required to pass through designated wheels wash facilities; and • Continuous water spray at the loading points. 	All construction sites	N/A (Construction in process)
Construction Noise (Air borne)				
S6.4.10 of HKBCFEIA	N1	Use of good site practices to limit noise emissions by considering the following: <ul style="list-style-type: none"> • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; • machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction, where possible, be orientated 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		so that the noise is directed away from nearby NSRs; <ul style="list-style-type: none"> • silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; • mobile plant should be sited as far away from NSRs as possible and practicable; • material stockpiles, mobile container site officer and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 		
S6.4.11 of HKBCFEIA	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	All construction sites	V
S6.4.12 of HKBCFEIA	N3	Install movable noise barriers (typically density @14kg/m ²), acoustic mat or full enclosure close to noisy plants including air compressor, generators, saw.	For plant items listed in Appendix 6D of the EIA report at all construction sites	N/A
S6.4.13 of HKBCFEIA	N4	Select “Quiet plants” which comply with the BS 5228 Part 1 or TM standards.	For plant items listed in Appendix 6D of the EIA report at all construction sites	V
S6.4.14 of HKBCFEIA	N5	Sequencing operation of construction plants where practicable.	All construction sites where practicable	V
S5.1 of	N6	Implement a noise monitoring under EM&A programme.	Selected	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
TMCLKLEIA			representative noise monitoring station	
Waste Management (Construction Waste)				
S12.6 of TMCLKLEIA	WM1	The Contractor shall identify a coordinator for the management of waste.	All construction sites	V
S12.6 of TMCLKLEIA	WM2	The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	All construction sites	V
S12.6 of TMCLKLEIA	WM3	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All construction sites	V
S8.3.8 of HKBCFEIA and S12.6 of TMCLKLEIA	WM4	<p><u>Construction and Demolition Material</u></p> <p>The following mitigation measures should be implemented in handling the waste:</p> <ul style="list-style-type: none"> • Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; • Carry out on-site sorting; • Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; • Adopt ‘Selective Demolition’ technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; • Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – “Environmental Management on Construction Sites” to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction; • In addition, disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation; and • The surplus surcharge should be transferred to a fill bank. 		
S8.3.9- S8.3.11 of HKBCFEIA and S12.6 of TMCLKLEIA	WM5	<p><u>C&D Waste</u></p> <ul style="list-style-type: none"> • Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding and falsework should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. • The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.</p>		
<p>S8.2.12- S8.3.15 of HKBCFEIA and S12.6 of TMCLKLEIA</p>	<p>WM6</p>	<p><u>Chemical Waste</u></p> <ul style="list-style-type: none"> • Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. • Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 liters unless the specification has been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation. • The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste; enclosed on at least 3 sides; have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20 % of the total volume of waste stored in that area, whichever is the greatest; have adequate ventilation; covered to prevent rainfall entering; and arranged so that incompatible materials are adequately separated. • Disposal of chemical waste should be via a licensed waste collector; be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre 	<p>All construction sites</p>	<p>V</p>

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		which also offers a chemical waste collection service and can supply the necessary storage containers; or be to a reuser of the waste, under approval from the EPD.		
S8.3.16 of HKBCFEIA and S12.6 of TMCLKLEIA	WM7	<u>Sewage</u> <ul style="list-style-type: none"> • Adequate numbers of portable toilets should be provided for the workers. The portable toilets should be maintained in a state, which will not deter the workers from utilizing these portable toilets. Night soil should be collected by licensed collectors regularly. 	All construction sites	V
S8.3.17 of HKBCFEIA and S12.6 of TMCLKLEIA	WM8	<u>General Refuse</u> <ul style="list-style-type: none"> • The site and surroundings shall be kept tidy and litter free. General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. • A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. • Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible. • Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>considered by the Contractor. In addition, waste separation facilities for paper, aluminum cans, plastic bottles etc., should be provided.</p> <ul style="list-style-type: none"> • Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including reduction, reuse and recycling of wastes. • Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. • All waste containers shall be in a secure area on hardstanding. 		
Water Quality (Construction Phase)				
	W1	<p>Mitigation during the marine works to reduce impacts to within acceptable levels have been recommended and will comprise a series of measures that restrict the method and sequencing of backfilling, as well as protection measures. Details of the measures are provided below:</p>	During filling	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Reclamation filling for the Project shall not proceed until at least 200m of leading seawall at the reclamation area formed above +2.2mPD, unless otherwise agreement was obtained from EPD, except for the 300m gaps for marine access. All underwater filling works shall be carried out behind seawalls to avoid dispersion of suspended solids outside the Project limit; • Except for the filling of the cellular structures, not more than 15% public fill shall be used for reclamation filling below +2.5mPD during construction of the seawall; • After the seawall is completed except for the 300m marine access as indicated in the EPs, not more than 30% public fill shall be used for reclamation filling below +2.5mPD, unless otherwise agreement from EPD was obtained; • Upon completion of 200m leading seawall, no more than a total of 60 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 60,000 m³ for HKBCF and TMCLKL southern landfall reclamation during the filling operation; and • Upon completion of the whole section of seawall except for the 300m marine access as indicated in the EPs, no more than a total of 190 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 190,000 m³ for the remaining filling operations for HKBCF and TMCLKL southern landfall reclamation. • Floating type perimeter silt curtains shall be around the HKBCF site before the commencement of marine works. Staggered layers of silt curtain shall be provided 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>to prevent sediment loss at navigation accesses. The length of each staggered layers shall be at least 200m;</p> <ul style="list-style-type: none"> • Single layer silt curtain to be applied around the North-east airport water intake; • The silt-curtains should be maintained in good condition to ensure the sediment plume generated from filling be confined effectively within the site boundary; • The filling works shall be scheduled to spread the works evenly over a working day; • Cellular structure shall be used for seawall construction; • A layer of geotextile shall be placed on top of the seabed before any filling activities take place inside the cellular structures to form the seawall; • The conveyor belts shall be fitted with windboards and conveyor release points shall be covered with curtain to prevent any spillage of filling materials onto the surrounding waters; and • An additional layer of silt curtain shall be installed near the active stone column installation points. A layer of geotextile with stone blanket on top shall be placed on the seabed prior to stone column installation works. 		
S9.11.1.3 of HKBCFEIA and S6.10 of	W2	<p><u>Land Works</u></p> <p>General construction activities on land should also be governed by standard good working practice. Specific measures to be written into the works contracts should include:</p>	All land-based construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
TMCLKLEIA		<ul style="list-style-type: none"> • wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters; • sewage effluent and discharges from on-site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided; • storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks; • silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm; • temporary access roads should be surfaced with crushed stone or gravel; • rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities; • measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system; • open stockpiles of construction materials (e.g. aggregates and sand) on site 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>should be covered with tarpaulin or similar fabric during rainstorms;</p> <ul style="list-style-type: none"> • manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers; • discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system; • all vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit; • wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain; • the section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel; • wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects; • vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for offsite disposal; 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • the contractors shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately; • waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance; • all fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank; and • surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the storm water system.. 		
S9.14 of HKBCFEIA and S6.10 of TMCLKLEIA	W3	Implement a water quality monitoring programme	At identified monitoring location	V
S6.10 of TMCLKLEIA	W4	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All construction site areas	V
Ecology (Construction Phase)				
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E1	<ul style="list-style-type: none"> • Install silt curtain during the construction • Limit works fronts • Construct seawall prior to reclamation filling where practicable 	Seawall, reclamation area	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Good site practices • Strict enforcement of no marine dumping • Site runoff control • Spill response plan 		
S10.7 of HKBCFEIA	E2	<ul style="list-style-type: none"> • Watering to reduce dust generation; prevention of siltation of freshwater habitats; Site runoff should be desilted, to reduce the potential for suspended sediments, organics and other contaminants to enter streams and standing freshwater. 	Land-based works areas	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E3	<ul style="list-style-type: none"> • Good site practices, including strictly following the permitted works hours, using quieter machines where practicable, and avoiding excessive lightings during night time. 	Land-based works areas	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E4	<ul style="list-style-type: none"> • Dolphin Exclusion Zone • Dolphin watching plan 	Marine works	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E5	<ul style="list-style-type: none"> • Decouple compressors and other equipment on working vessels • Proposal on design and implementation of acoustic decoupling measures applied during reclamation works • Avoidance of percussive piling 	Marine works	V
S10.7 of	E6	<ul style="list-style-type: none"> • Control vessel speed 	Marine traffic	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
HKBCFEIA and S8.14 of TMCLKLEIA		<ul style="list-style-type: none"> • Skipper training • Predefined and regular routes for working vessels; avoid Brothers Islands 		
S10.10 of HKBCFEIA and S8.14 of TMCLKLEIA	E7	<ul style="list-style-type: none"> • Vessel based dolphin monitoring 	Northeast and Northwest Lantau	V
Fisheries				
S11.7 of HKBCFEIA	F1	<ul style="list-style-type: none"> • Reduce re-suspension of sediments • Limit works fronts • Good site practices • Strict enforcement of no marine dumping • Spill response plan 	Seawall, reclamation area	V
S11.7 of HKBCFEIA	F2	<ul style="list-style-type: none"> • Install silt-grease trap in the drainage system collecting surface runoff 	Reclamation area	V
Landscape & Visual (Construction Phase)				
S14.3.3. 3 of HKBCFEIA and S10.9 of TMCLKLEIA	LV1	<p><u>Mitigate Landscape Impacts</u></p> <p>G1/CM4 Grass-hydroseed or sheeting bare soil surface and stock pile areas.</p> <p>G9 Reserve of loose natural granite rocks for re-use. Provide new coastline to adopt “natural-look” by means of using armour rocks in the form of natural</p>	All construction site areas	N/A

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		rock materials and planting strip area accommodating screen buffer to enhance “natural-look” of new coastline.		
S10.9 of TMCLKLEIA	LV2	<u>Mitigate Landscape Impacts</u> CM7 Ensure no run-off into water body adjacent to the Project Area.	All construction site areas	V
S14.3.3. 3 of HKBCFEIA	LV4	<u>Mitigate Visual Impacts</u> V1 Minimize time for construction activities during construction period.	All construction site areas	V
S10.9 of TMCLKLEIA	LV5	<u>Mitigate Visual Impacts</u> CM6 Control night-time lighting and glare by hooding all lights.	All construction site areas	V
EM&A				
S15.2.2 of HKBCFEIA	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	All construction site areas	V
S15.5 - S15.6 of HKBCFEIA	EM2	<ul style="list-style-type: none"> An Environmental Team needs to be employed as per the EM&A Manual. Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	All construction site areas	V

Legend: V = implemented;

x = not implemented;

N/A = not applicable

Appendix D - Summary of Action and Limit Levels

Table 1 – Action and Limit Levels for 1-hour TSP

Location	Action Level	Limit Level
AMS2	374 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS3B*	368 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS6	360 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS7A [#]	370 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$

Remarks: * Action Level set out at AMS3 Ho Yu College is adopted.

[#]Action level set out at AMS7 Hong Kong SkyCity Marriott Hotel is adopted.

Table 2 – Action and Limit Levels for 24-hour TSP

Location	Action Level	Limit Level
AMS2	176 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS3B*	167 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS6	173 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS7A [#]	183 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$

Remarks: * Action Level set out at AMS3 Ho Yu College is adopted.

[#]Action level set out at AMS7 Hong Kong SkyCity Marriott Hotel is adopted.

Table 3 – Action and Limit Levels for Construction Noise (0700-1900 hrs of normal weekdays)

Location	Action Level	Limit Level
NMS2	When one documented complaint, related to 0700 – 1900 hours on normal weekdays, is received from any one of the sensitive receivers	75 dB(A)
NMS3B		*65 / 70 dB(A)

*Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

Table 4 – Action and Limit Levels for Water Quality

Parameters	Action	Limit
DO in mg L ⁻¹ (Surface, Middle & Bottom)	<u>Surface and Middle</u> 5.0 <u>Bottom</u> 4.7	<u>Surface and Middle</u> 4.2 (except 5 mg/L for FCZ) <u>Bottom</u> 3.6
SS in mg L ⁻¹ (depth-averaged)	23.5 and 120% of upstream control station's SS at the same tide of the same day	34.4 and 130% of upstream control station's SS at the same tide of the same day and 10mg/L for WSD Seawater intakes
Turbidity in NTU (depth-averaged)	27.5 and 120% of upstream control station's turbidity at the same tide of the same day	47.0 and 130% of upstream control station's turbidity at the same tide of the same day

Notes:

1. "depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.
2. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
3. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table 5(a) Action and Limit Levels for Chinese White Dolphin Monitoring - Approach to Define Action Level (AL) and Limit Level (LL):

	North Lantau Social Cluster	
	NEL	NWL
Action Level	(STG < 70% of baseline) & (ANI < 70% of baseline)	(STG < 70% of baseline) & (ANI < 70% of baseline)
Limit Level	[(STG < 40% of baseline) & (ANI < 40% of baseline)] AND [(STG < 40% of baseline) & (ANI < 40% of baseline)]	

For North Lantau Social Cluster, action level will be trigger if either NEL **or** NWL fall below the criteria; limit level will be triggered if both NEL **and** NWL fall below the criteria.

Table 5(b) Derived Value of Action Level (AL) and Limit Level (LL) for Chinese White Dolphin Monitoring

	North Lantau Social Cluster	
	NEL	NWL
Action Level	(STG < 4.2) & (ANI < 15.5)	(STG < 6.9) & (ANI < 31.3)
Limit Level	[(STG < 2.4) & (ANI < 8.9)] AND [(STG < 3.9)& (ANI < 17.9)]	

AECOM Asia Company Limited

TSP High Volume Sampler

Field Calibration Report

Station: Tung Chung Development Pier (AMS2) Operator: Leung Yiu Ting
 Cal. Date: 26-Nov-15 Next Due Date: 26-Jan-16
 Equipment No.: A-001-78T Serial No.: 3383

Ambient Condition			
Temperature, Ta (K)	294	Pressure, Pa (mmHg)	764.2

Orifice Transfer Standard Information					
Serial No:	843	Slope, mc	1.99924	Intercept, bc	-0.01238
Last Calibration Date:	9-Dec-14	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	9-Dec-15	$Qstd = \{[DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] ^{1/2}	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	8.1	2.87	1.44	49.0	49.47
13	6.9	2.65	1.33	44.0	44.42
10	5.0	2.26	1.14	37.0	37.35
7	4.0	2.02	1.02	32.0	32.31
5	2.6	1.63	0.82	24.0	24.23

By Linear Regression of Y on X
 Slope, mw = 39.9977 Intercept, bw = -8.4251
 Correlation Coefficient* = 0.9990
 *If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 1.30m³/min
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 43.16

Remarks: _____

QC Reviewer: WS CHAN Signature: [Signature] Date: 26/11/15

AECOM Asia Company Limited
TSP High Volume Sampler
Field Calibration Report

Station Site Boundary of Site Office (WA2) (AMS3B) Operator: Leung Yiu Ting
 Cal. Date: 5-Nov-15 Next Due Date: 5-Jan-16
 Equipment No.: A-001-79T Serial No. 3384

Ambient Condition			
Temperature, Ta (K)	301.5	Pressure, Pa (mmHg)	760.8

Orifice Transfer Standard Information					
Serial No:	843	Slope, mc	1.99924	Intercept, bc	-0.01238
Last Calibration Date:	9-Dec-14	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	9-Dec-15	$Qstd = \{[DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	$[DH \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	7.1	2.65	1.33	48.0	47.75
13	6.0	2.44	1.22	43.0	42.77
10	4.8	2.18	1.10	37.0	36.80
7	3.2	1.78	0.90	24.0	23.87
5	2.1	1.44	0.73	16.0	15.92

By Linear Regression of Y on X

Slope, mw = 53.9741 Intercept, bw = -23.5369

Correlation Coefficient* = 0.9961

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 1.30m³/min

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 46.88

Remarks: _____

QC Reviewer: WS CHAN Signature: [Signature] Date: 05/11/15

AECOM Asia Company Limited

TSP High Volume Sampler

Field Calibration Report

Station: Chu Kong Air-Sea Union Transportation Co.Ltd. (AMS7A) Operator: Cheung Hung Wai
 Cal. Date: 30-Nov-15 Next Due Date: 30-Jan-16
 Equipment No.: A-001-80T Serial No.: 3385

Ambient Condition			
Temperature, Ta (K)	297.0	Pressure, Pa (mmHg)	762.9

Orifice Transfer Standard Information					
Serial No:	843	Slope, mc	1.99924	Intercept, bc	-0.01238
Last Calibration Date:	9-Dec-14	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	9-Dec-15	$Qstd = \{ [DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc \} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] ^{1/2}	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	7.0	2.66	1.33	48.0	48.17
13	6.0	2.46	1.24	42.0	42.15
10	4.7	2.18	1.09	34.0	34.12
7	3.5	1.88	0.95	26.0	26.09
5	2.7	1.65	0.83	20.0	20.07

By Linear Regression of Y on X
 Slope, mw = 55.6589 Intercept, bw = -26.4455
 Correlation Coefficient* = 0.9993
 *If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 1.30m³/min
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 45.75

Remarks: _____

QC Reviewer: WIS CHAN Signature: [Signature] Date: 30/11/15



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELS, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - May 29, 2015 Rootmeter S/N 0438320 Ta (K) - 297
 Operator Tisch Orifice I.D. - 0988 Pa (mm) - 755.65

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3980	3.2	2.00
2	NA	NA	1.00	0.9910	6.3	4.00
3	NA	NA	1.00	0.8790	7.8	5.00
4	NA	NA	1.00	0.8380	8.6	5.50
5	NA	NA	1.00	0.6890	12.6	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9934	0.7106	1.4125	0.9957	0.7123	0.8866
0.9893	0.9983	1.9976	0.9917	1.0007	1.2539
0.9872	1.1231	2.2334	0.9896	1.1258	1.4019
0.9862	1.1769	2.3424	0.9886	1.1797	1.4703
0.9809	1.4237	2.8251	0.9833	1.4271	1.7732
Qstd slope (m) = 1.97831			Qa slope (m) = 1.23878		
intercept (b) = 0.01264			intercept (b) = 0.00793		
coefficient (r) = 0.99985			coefficient (r) = 0.99985		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b }
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b }

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.07a
 Sensitivity Adjustment Scale Setting: 557 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 557 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 557 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	08-05-15	09:15 - 10:15	26.9	76	0.04417	1763	29.38
2	08-05-15	10:15 - 11:15	26.9	76	0.04625	1851	30.85
3	08-05-15	11:15 - 12:15	26.9	77	0.04513	1805	30.08
4	08-05-15	12:15 - 13:15	27.1	77	0.04828	1926	32.10

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9983

Validity of Calibration Record: 8 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 11 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.08a
 Sensitivity Adjustment Scale Setting: 702 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 702 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 702 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	08-05-15	09:30 - 10:30	26.9	76	0.04587	1722	28.70
2	08-05-15	10:30 - 11:30	26.9	76	0.04774	1795	29.92
3	08-05-15	11:30 - 12:30	26.9	77	0.04976	1864	31.07
4	08-05-15	12:30 - 13:30	27.1	77	0.05051	1901	31.68

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0016
 Correlation coefficient: 0.9978

Validity of Calibration Record: 8 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 11 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.09a
 Sensitivity Adjustment Scale Setting: 797 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 797 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 797 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	08-05-15	13:15 - 14:15	27.1	77	0.04986	1994	33.23
2	08-05-15	14:15 - 15:15	27.1	77	0.05083	2037	33.95
3	08-05-15	15:15 - 16:15	27.1	77	0.05012	2003	33.38
4	08-05-15	16:15 - 17:15	27.1	76	0.05241	2095	34.92

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9968

Validity of Calibration Record: 8 May 2016

Remarks:

QC Reviewer: YW Fung

Signature: 

Date: 11 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.10a
 Sensitivity Adjustment Scale Setting: 753 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 753 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 753 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	08-05-15	13:45 - 14:45	27.1	77	0.04963	1989	33.15
2	08-05-15	14:45 - 15:45	27.1	77	0.05131	2054	34.23
3	08-05-15	15:45 - 16:45	27.1	77	0.05170	2066	34.43
4	08-05-15	16:45 - 17:45	27.1	77	0.05269	2110	35.17

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9974

Validity of Calibration Record: 8 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 11 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.11a
 Sensitivity Adjustment Scale Setting: 799 CPM
 Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 799 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 799 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	13-05-15	09:15 - 10:15	27.3	78	0.04635	1853	30.88
2	13-05-15	10:15 - 11:15	27.3	78	0.04788	1916	31.93
3	13-05-15	11:15 - 12:15	27.3	78	0.04943	1985	33.08
4	13-05-15	12:15 - 13:15	27.4	78	0.05176	2075	34.58

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9983

Validity of Calibration Record: 13 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 14 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.13a
 Sensitivity Adjustment Scale Setting: 643 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 643 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 643 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	13-05-15	09:45 - 10:45	27.3	78	0.04654	1867	31.12
2	13-05-15	10:45 - 11:45	27.3	78	0.04743	1901	31.68
3	13-05-15	11:45 - 12:45	27.3	78	0.05036	2010	33.50
4	13-05-15	12:45 - 13:45	27.4	78	0.05271	2112	35.20

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9984

Validity of Calibration Record: 13 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 14 May 2015

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.14a
 Sensitivity Adjustment Scale Setting: 786 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 7 May 2015

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 786 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 786 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	13-05-15	13:15 - 14:15	27.4	78	0.05084	2178	36.30
2	13-05-15	14:15 - 15:15	27.5	78	0.05236	2243	37.38
3	13-05-15	15:15 - 16:15	27.5	78	0.05345	2295	38.25
4	13-05-15	16:15 - 17:15	27.4	77	0.05272	2261	37.68

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0014
 Correlation coefficient: 0.9972

Validity of Calibration Record: 13 May 2016

Remarks:

QC Reviewer: YW Fung Signature:  Date: 14 May 2015



CERTIFICATE OF CALIBRATION

Certificate No.: 15CA0303 01-02

Page: 1 of 2

Item tested

Description: Acoustical Calibrator (Class 1)
Manufacturer: B & K
Type/Model No.: 4231
Serial/Equipment No.: 3006428
Adaptors used: -

Item submitted by

Customer: AECOM ASIA CO LIMITED
Address of Customer: -
Request No.: -
Date of receipt: 03-Mar-2015

Date of test: 03-Mar-2015

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2412857	13-May-2015	SCL
Preamplifier	B&K 2673	2743150	10-Apr-2015	CEPREI
Measuring amplifier	B&K 2610	2346941	08-Apr-2015	CEPREI
Signal generator	DS 360	61227	09-Apr-2015	CEPREI
Digital multi-meter	34401A	US36087050	01-Dec-2015	CEPREI
Audio analyzer	8903B	GB41300350	07-Apr-2015	CEPREI
Universal counter	53132A	MY40003662	11-Apr-2015	CEPREI

Ambient conditions

Temperature: 21 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1010 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:

Huang Jian Min/Feng Jun Qi

Date: 04-Mar-2015

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



CERTIFICATE OF CALIBRATION

Certificate No.: 15CA0317 03 Page 1 of 2

Item tested

Description:	Sound Level Meter (Type 1)	,	Microphone
Manufacturer:	B & K	,	B & K
Type/Model No.:	2238	,	4188
Serial/Equipment No.:	2285692	,	2791211
Adaptors used:	-	,	-

Item submitted by

Customer Name: AECOM ASIA CO., LTD.
Address of Customer: -
Request No.: -
Date of receipt: 17-Mar-2015

Date of test: 18-Mar-2015

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	20-Jun-2015	CIGISMEC
Signal generator	DS 360	33873	09-Apr-2015	CEPREI
Signal generator	DS 360	61227	09-Apr-2015	CEPREI

Ambient conditions

Temperature: 21 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1010 ± 5 hPa

Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responses of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

Huang Jian Min/Feng Jun Qi

Date: 19-Mar-2015

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1541932
Sub-batch: 0
Date of Issue: 05/11/2015
Client: AECOM ASIA COMPANY LIMITED



Description: Multifunctional Meter
Brand Name: YSI
Model No.: Sonde 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35
Date of Calibration: 03 November, 2015

Date of next Calibration: 03 February, 2016

Parameters:

Conductivity

Method Ref: APHA (21th edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	145.8	-0.7
6667	6710	+0.6
12890	12710	-1.4
58670	58780	+0.2
Tolerance Limit (%)		±10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.50	3.48	-0.02
5.75	5.78	+0.03
7.70	7.66	-0.04
Tolerance Limit (mg/L)		±0.20

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)
10.5	10.47	-0.0
22.0	21.95	-0.1
37.0	36.86	-0.1
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.



 Mr Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1541932
Sub-batch: 0
Date of Issue: 05/11/2015
Client: AECOM ASIA COMPANY LIMITED



Description: Multifunctional Meter
Brand Name: YSI
Model No.: Sonde 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35

Date of Calibration: 03 November, 2015 **Date of next Calibration:** 03 February, 2016

Parameters:

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)
0	0.0	--
10	9.95	-0.5
20	19.97	-0.2
30	29.92	-0.3
Tolerance Limit (%)		±10.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	4.0	0.0
10	10.3	+3.0
20	20.2	+1.0
50	50.4	+0.8
100	99.6	-0.4
Tolerance Limit (%)		±10.0

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.00	0.00
7.0	7.02	+0.02
10.0	10.01	+0.01
Tolerance Limit (pH Unit)		±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.


 Mr Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1541933
Sub-batch: 0
Date of Issue: 05/11/2015
Client: AECOM ASIA COMPANY LIMITED



Description: Multifunctional Meter
Brand Name: YSI
Model No.: Sonde 6820 V2
Serial No.: 12D100972
Equipment No.: W.026.36
Date of Calibration: 03 November, 2015

Date of next Calibration: 03 February, 2016

Parameters:

Conductivity

Method Ref: APHA (21th edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	145.2	-1.2
6667	6690	+0.3
12890	12850	-0.3
58670	58700	+0.1
Tolerance Limit (%)		±10.0

Dissolved Oxygen Method Ref: APHA (21st edition), 4500O: G


Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.50	3.51	+0.01
5.75	5.72	-0.03
7.70	7.67	-0.03
Tolerance Limit (mg/L)		±0.20

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)
10.5	10.51	+0.0
22.0	22.05	+0.1
37.0	36.89	-0.1
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.


 Mr Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1541933
 Sub-batch: 0
 Date of Issue: 05/11/2015
 Client: AECOM ASIA COMPANY LIMITED



Description: Multifunctional Meter
 Brand Name: YSI
 Model No.: Sonde 6820 V2
 Serial No.: 12D100972
 Equipment No.: W.026.36
 Date of Calibration: 03 November, 2015

Date of next Calibration: 03 February, 2016

Parameters:

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)
0	0.0	--
10	10.04	+0.4
20	20.06	+0.3
30	30.04	+0.1
Tolerance Limit (%)		±10.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	4.1	+2.5
10	10.2	+2.0
20	20.2	+1.0
50	50.5	+1.0
100	99.3	-0.7
Tolerance Limit (%)		±10.0

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.01	+0.01
7.0	7.03	+0.03
10.0	9.98	-0.02
Tolerance Limit (pH Unit)		±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.


 Mr Fung Lim Chee, Richard
 General Manager -
 Greater China & Hong Kong

**Hong Kong Boundary Crossing Facilities – Reclamation Works
Impact Monitoring Schedule for December 2015**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		01-Dec	02-Dec	03-Dec	04-Dec	05-Dec
		Dolphin monitoring	Mid-Flood 12:40 Mid-Ebb 17:56 Dolphin monitoring	24-hour TSP 1-hour TSP Noise	Mid-Ebb 06:35 Mid-Flood 14:31	
06-Dec	07-Dec	08-Dec	09-Dec	10-Dec	11-Dec	12-Dec
	Mid-Ebb 10:19 Mid-Flood 16:18 Dolphin monitoring	Dolphin monitoring	Mid-Ebb 11:44 Mid-Flood 17:14 24-hour TSP 1-hour TSP Noise		Mid-Flood 07:37 Mid-Ebb 13:02	
13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec
	Mid-Flood 09:38 Mid-Ebb 15:05 24-hour TSP 1-hour TSP Noise		Mid-Flood 11:11 Mid-Ebb 16:44		Mid-Ebb 05:21 Mid-Flood 12:59 24-hour TSP 1-hour TSP	
20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec
	Mid-Ebb 09:02 Mid-Flood 15:29		Mid-Ebb 11:17 Mid-Flood 16:53	24-hour TSP 1-hour TSP Noise	Mid-Flood 07:36 Mid-Ebb 12:59	
27-Dec	28-Dec	29-Dec	30-Dec	31-Dec		
	Mid-Flood 09:43 Mid-Ebb 15:00		Mid-Flood 11:00 Mid-Ebb 16:19 24-hour TSP 1-hour TSP Noise			

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

**Hong Kong Boundary Crossing Facilities – Reclamation Works
Tentative Impact Monitoring Schedule for January 2016**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					01-Jan	02-Jan
					Mid-Flood 12:19 Mid-Ebb 18:06	
03-Jan	04-Jan	05-Jan	06-Jan	07-Jan	08-Jan	09-Jan
	Mid-Ebb 07:42 Mid-Flood 14:33 24-hour TSP 1-hour TSP Noise		Mid-Ebb 10:29 Mid-Flood 15:53	Dolphin monitoring	Mid-Ebb 12:04 Mid-Flood 17:14 Dolphin monitoring	24-hour TSP 1-hour TSP
10-Jan	11-Jan	12-Jan	13-Jan	14-Jan	15-Jan	16-Jan
	Mid-Flood 08:42 Mid-Ebb 14:07		Mid-Flood 09:57 Mid-Ebb 15:34 24-hour TSP 1-hour TSP Noise		Mid-Flood 11:21 Mid-Ebb 17:18	
17-Jan	18-Jan	19-Jan	20-Jan	21-Jan	22-Jan	23-Jan
	Mid-Ebb 07:12 Mid-Flood 13:55 Dolphin monitoring	24-hour TSP 1-hour TSP Noise Dolphin monitoring	Mid-Ebb 10:13 Mid-Flood 15:45		Mid-Ebb 12:06 Mid-Flood 17:20	
24-Jan	25-Jan	26-Jan	27-Jan	28-Jan	29-Jan	30-Jan
	Mid-Flood 08:39 Mid-Ebb 14:00 24-hour TSP 1-hour TSP Noise		Mid-Flood 09:35 Mid-Ebb 15:02		Mid-Flood 10:27 Mid-Ebb 16:11	24-hour TSP 1-hour TSP
31-Jan						

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

Appendix G Impact Air Quality Monitoring Results

1-hour TSP Monitoring Results at Station AMS2 - Tung Chung Development Pier

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. (µg/m ³)	Action Level (µg/m ³)	Limit Level (µg/m ³)
03-Dec-15	1st Hour	Fine	0.07	10:00	72	374	500
03-Dec-15	2nd Hour	Fine	N.A.	11:00	72	374	500
03-Dec-15	3rd Hour	Fine	N.A.	12:00	73	374	500
09-Dec-15	1st Hour	Fine	N.A.	11:42	82	374	500
09-Dec-15	2nd Hour	Fine	N.A.	12:42	80	374	500
09-Dec-15	3rd Hour	Fine	N.A.	13:42	82	374	500
14-Dec-15	1st Hour	Cloudy	2.77	10:25	79	374	500
14-Dec-15	2nd Hour	Cloudy	0.17	11:25	78	374	500
14-Dec-15	3rd Hour	Cloudy	0.11	12:25	78	374	500
18-Dec-15	1st Hour	Sunny	0.06	12:00	74	374	500
18-Dec-15	2nd Hour	Sunny	0.15	13:00	76	374	500
18-Dec-15	3rd Hour	Sunny	0.07	14:00	76	374	500
24-Dec-15	1st Hour	Fine	0.06	10:50	73	374	500
24-Dec-15	2nd Hour	Fine	0.24	11:50	72	374	500
24-Dec-15	3rd Hour	Fine	1.54	12:50	73	374	500
30-Dec-15	1st Hour	Fine	0.10	10:00	73	374	500
30-Dec-15	2nd Hour	Fine	0.10	11:00	72	374	500
30-Dec-15	3rd Hour	Fine	0.07	12:00	73	374	500
					Average	75	
					Min	72	
					Max	82	

1-hour TSP Monitoring Results at Station AMS3B - Site Boundary of Site Office (WA2)

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. (µg/m ³)	Action Level (µg/m ³) ^	Limit Level (µg/m ³)
03-Dec-15	1st Hour	Fine	0.07	10:15	70	368	500
03-Dec-15	2nd Hour	Fine	N.A.	11:15	71	368	500
03-Dec-15	3rd Hour	Fine	N.A.	12:15	71	368	500
09-Dec-15	1st Hour	Fine	N.A.	10:10	79	368	500
09-Dec-15	2nd Hour	Fine	N.A.	11:10	78	368	500
09-Dec-15	3rd Hour	Fine	N.A.	12:10	78	368	500
14-Dec-15	1st Hour	Cloudy	0.17	11:43	77	368	500
14-Dec-15	2nd Hour	Cloudy	0.11	12:43	78	368	500
14-Dec-15	3rd Hour	Cloudy	0.06	13:43	80	368	500
18-Dec-15	1st Hour	Sunny	0.06	11:50	73	368	500
18-Dec-15	2nd Hour	Sunny	0.15	12:50	72	368	500
18-Dec-15	3rd Hour	Sunny	0.07	13:50	74	368	500
24-Dec-15	1st Hour	Fine	0.06	10:59	71	368	500
24-Dec-15	2nd Hour	Fine	0.24	11:59	73	368	500
24-Dec-15	3rd Hour	Fine	1.54	12:59	73	368	500
30-Dec-15	1st Hour	Fine	0.10	10:10	71	368	500
30-Dec-15	2nd Hour	Fine	0.10	11:10	73	368	500
30-Dec-15	3rd Hour	Fine	0.07	12:10	71	368	500
					Average	74	
					Min	70	
					Max	80	

Remarks:

^ Action Level set out at AMS3 Ho Yu College is adopted.

1-hour TSP Monitoring Results at Station AMS7A - Chu Kong Air-Sea Union Transportation Company Limited

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. (µg/m ³)	Action Level (µg/m ³)#	Limit Level (µg/m ³)
03-Dec-15	1st Hour	Fine	0.07	10:30	74	370	500
03-Dec-15	2nd Hour	Fine	N.A.	11:30	76	370	500
03-Dec-15	3rd Hour	Fine	N.A.	12:30	72	370	500
09-Dec-15	1st Hour	Fine	N.A.	12:19	82	370	500
09-Dec-15	2nd Hour	Fine	N.A.	13:19	82	370	500
09-Dec-15	3rd Hour	Fine	N.A.	14:19	80	370	500
14-Dec-15	1st Hour	Cloudy	2.77	10:04	78	370	500
14-Dec-15	2nd Hour	Cloudy	0.17	11:04	77	370	500
14-Dec-15	3rd Hour	Cloudy	0.11	12:04	78	370	500
18-Dec-15	1st Hour	Sunny	0.06	12:10	79	370	500
18-Dec-15	2nd Hour	Sunny	0.15	13:10	78	370	500
18-Dec-15	3rd Hour	Sunny	0.07	14:10	79	370	500
24-Dec-15	1st Hour	Fine	0.06	11:10	77	370	500
24-Dec-15	2nd Hour	Fine	0.24	12:10	77	370	500
24-Dec-15	3rd Hour	Fine	1.54	13:10	76	370	500
30-Dec-15	1st Hour	Fine	0.10	10:20	78	370	500
30-Dec-15	2nd Hour	Fine	0.10	11:20	78	370	500
30-Dec-15	3rd Hour	Fine	0.07	12:20	76	370	500
					Average	78	
					Min	72	
					Max	82	

Remarks:

Action Level set out at AMS7 Hong Kong SkyCity Marriott Hotel is adopted

*Due to malfunction of the wind data monitoring equipment, wind data was not able to be obtained for monitoring event(s) conducted between 10:13:35 3 Dec 2015 – 16:00:00 9 December 2015. Wind speed and direction dataset 10:13:35 3 Dec 2015 – 16:00:00 9 December 2015 from the Hong Kong Observatory is not available at time this monthly report is submitted.

Appendix G Impact Air Quality Monitoring Results

24-hour TSP Monitoring Results at Station AMS2 - Tung Chung Development Pier

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³)	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
02-Dec-15	16:00	03-Dec-15	16:00	Fine	20.8	1019.4	1.33	1.33	1.33	1912.3	2.8169	2.9200	0.1031	5688.04	5712.04	24.00	54	176	260
08-Dec-15	16:00	09-Dec-15	16:00	Fine	17.7	1016.8	1.33	1.33	1.33	1912.3	2.8150	2.9022	0.0872	5712.04	5736.04	24.00	46	176	260
14-Dec-15	09:00	15-Dec-15	09:00	Rainy	20.4	1016.6	1.33	1.33	1.33	1912.3	2.8237	2.9287	0.1050	5736.04	5760.04	24.00	55	176	260
17-Dec-15	16:00	18-Dec-15	16:00	Sunny	13.9	1026.4	1.33	1.33	1.33	1912.3	2.7965	2.9271	0.1306	5760.04	5784.04	24.00	68	176	260
23-Dec-15	16:00	24-Dec-15	16:00	Fine	22.3	1016.8	1.33	1.33	1.33	1912.3	2.8135	2.8944	0.0809	5784.04	5808.04	24.00	42	176	260
29-Dec-15	14:30	30-Dec-15	14:30	Cloudy	17.3	1025.3	1.33	1.33	1.33	1912.3	2.8096	2.9959	0.1863	5808.04	5832.04	24.00	97	176	260
																Average	60		
																Min	42		
																Max	97		

24-hour TSP Monitoring Results at Station AMS3B - Site Boundary of Site Office (WA2)

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³) [^]	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
02-Dec-15	16:00	03-Dec-15	16:00	Fine	20.8	1019.4	1.34	1.34	1.34	1923.8	2.8190	2.9090	0.0900	6463.38	6487.38	24.00	47	167	260
08-Dec-15	16:00	09-Dec-15	16:00	Fine	17.7	1016.8	1.34	1.34	1.34	1923.8	2.8210	2.9306	0.1096	6487.38	6511.38	24.00	57	167	260
14-Dec-15	09:00	15-Dec-15	09:00	Rainy	20.4	1016.6	1.34	1.34	1.34	1923.8	2.8224	2.8987	0.0763	6511.38	6535.38	24.00	40	167	260
17-Dec-15	16:00	18-Dec-15	16:00	Sunny	13.9	1026.4	1.34	1.34	1.34	1923.8	2.8030	2.8960	0.0930	6535.38	6559.38	24.00	48	167	260
23-Dec-15	16:00	24-Dec-15	16:00	Fine	22.3	1016.8	1.34	1.34	1.34	1923.8	2.7985	2.8608	0.0623	6559.38	6583.38	24.00	32	167	260
29-Dec-15	14:30	30-Dec-15	14:30	Cloudy	17.3	1025.3	1.34	1.34	1.34	1923.8	2.8112	2.9316	0.1204	6583.38	6607.38	24.00	63	167	260
																Average	48		
																Min	32		
																Max	63		




[^] Action Level set out at AMS3 Ho Yu College is adopted.

24-hour TSP Monitoring Results at Station AMS7A - Chu Kong Air-Sea Union Transportation Company Limited

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³) [#]	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
02-Dec-15	16:00	03-Dec-15	16:00	Fine	20.8	1019.4	1.30	1.30	1.30	1869.1	2.8316	2.9280	0.0964	5403.92	5427.92	24.00	52	183	260
08-Dec-15	16:00	09-Dec-15	16:00	Fine	17.7	1016.8	1.30	1.30	1.30	1868.3	2.8100	2.8894	0.0794	5427.92	5451.91	23.99	42	183	260
14-Dec-15	09:00	15-Dec-15	09:00	Rainy	20.4	1016.6	1.30	1.30	1.30	1869.1	2.8412	2.9262	0.0850	5451.91	5475.91	24.00	45	183	260
17-Dec-15	16:00	18-Dec-15	16:00	Sunny	13.9	1026.4	1.30	1.30	1.30	1869.1	2.7956	2.9172	0.1216	5475.91	5499.91	24.00	65	183	260
23-Dec-15	16:00	24-Dec-15	16:00	Fine	22.3	1016.8	1.30	1.30	1.30	1869.1	2.7946	2.8832	0.0886	5499.91	5523.91	24.00	47	183	260
29-Dec-15	14:30	30-Dec-15	14:30	Cloudy	17.3	1025.3	1.30	1.30	1.30	1869.1	2.8114	2.9328	0.1214	5523.91	5547.91	24.00	65	183	260
																Average	53		
																Min	42		
																Max	65		

Remarks:

[#] Action Level set out at AMS7 Hong Kong SkyCity Marriott Hotel is adopted

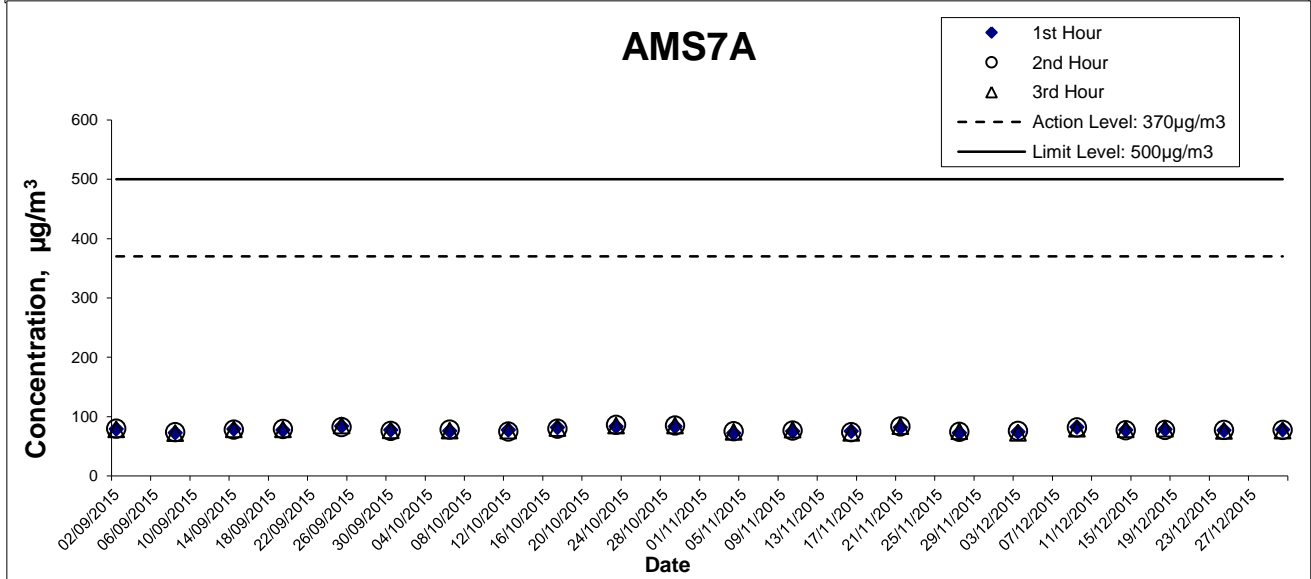
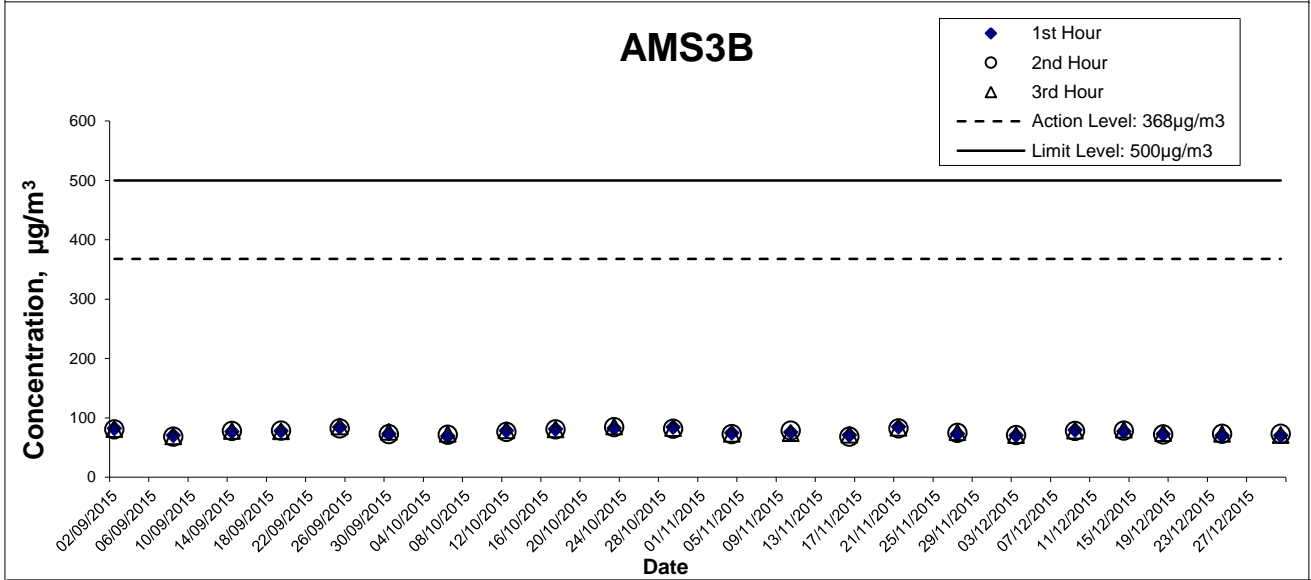
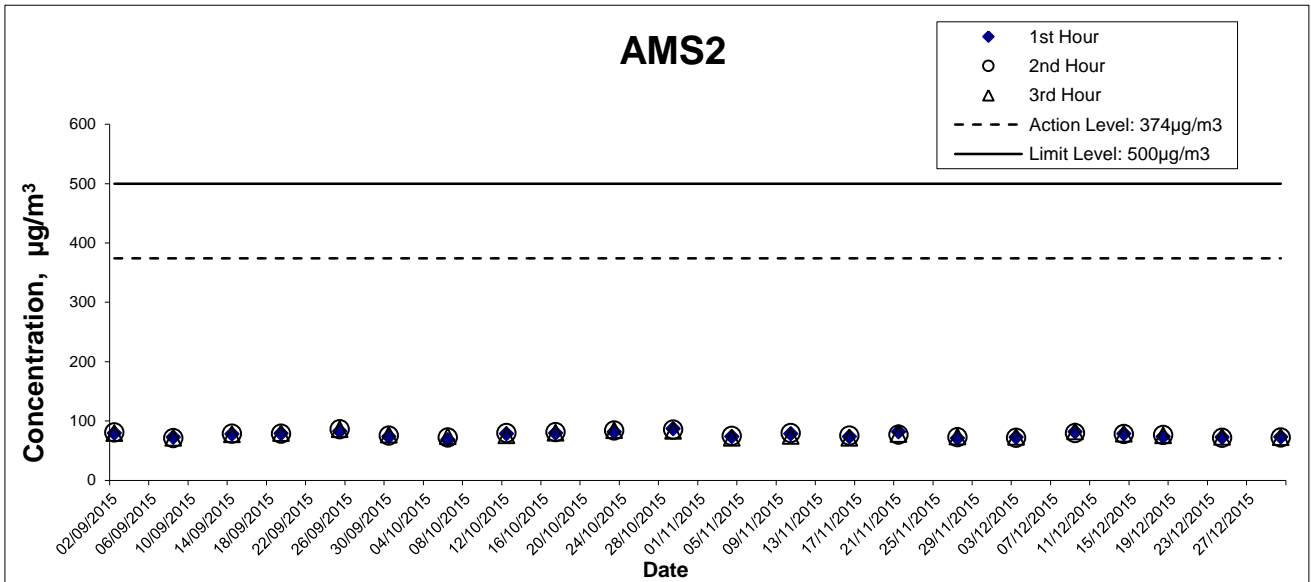


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

**Graphical Presentation of Impact 1-hour TSP
 Monitoring Results**



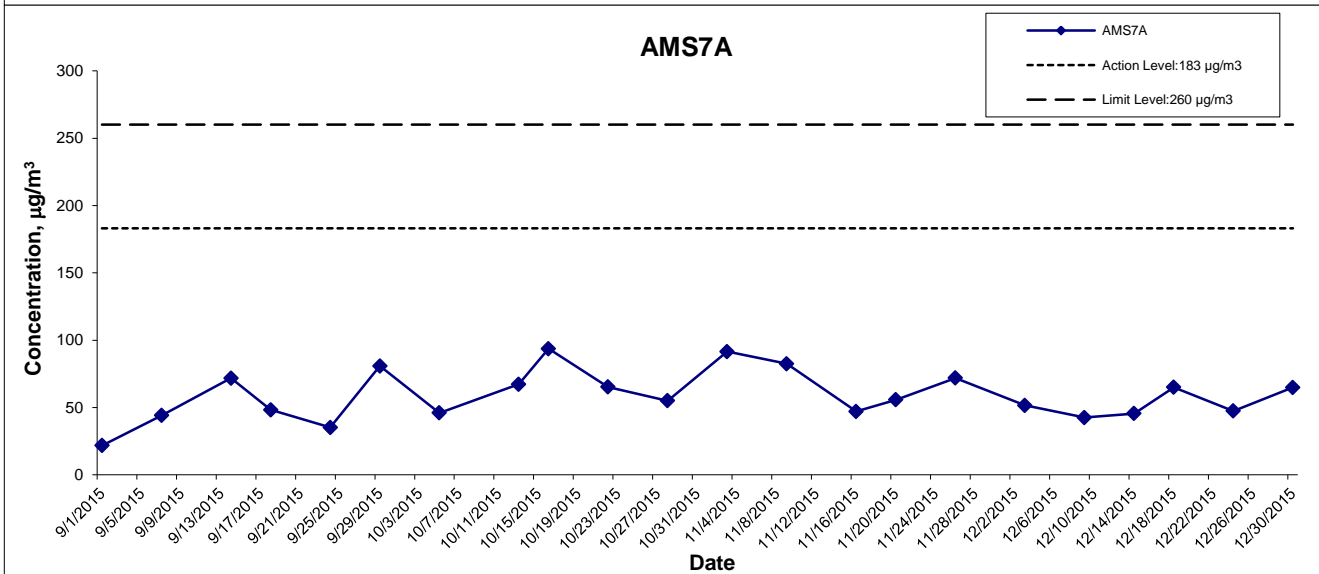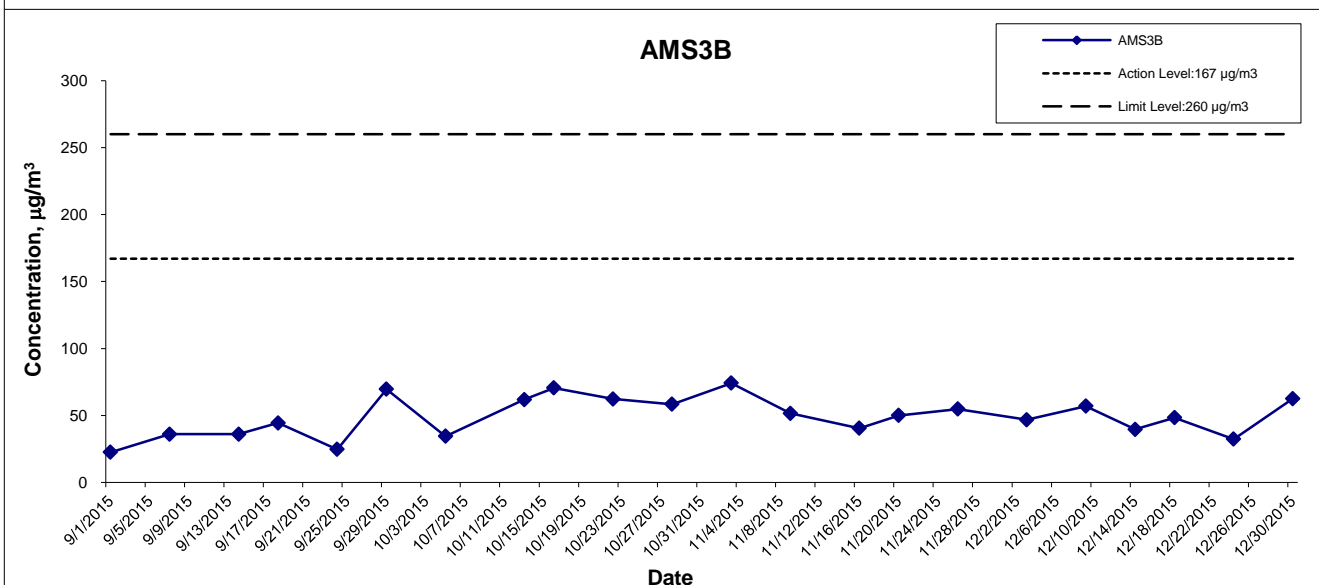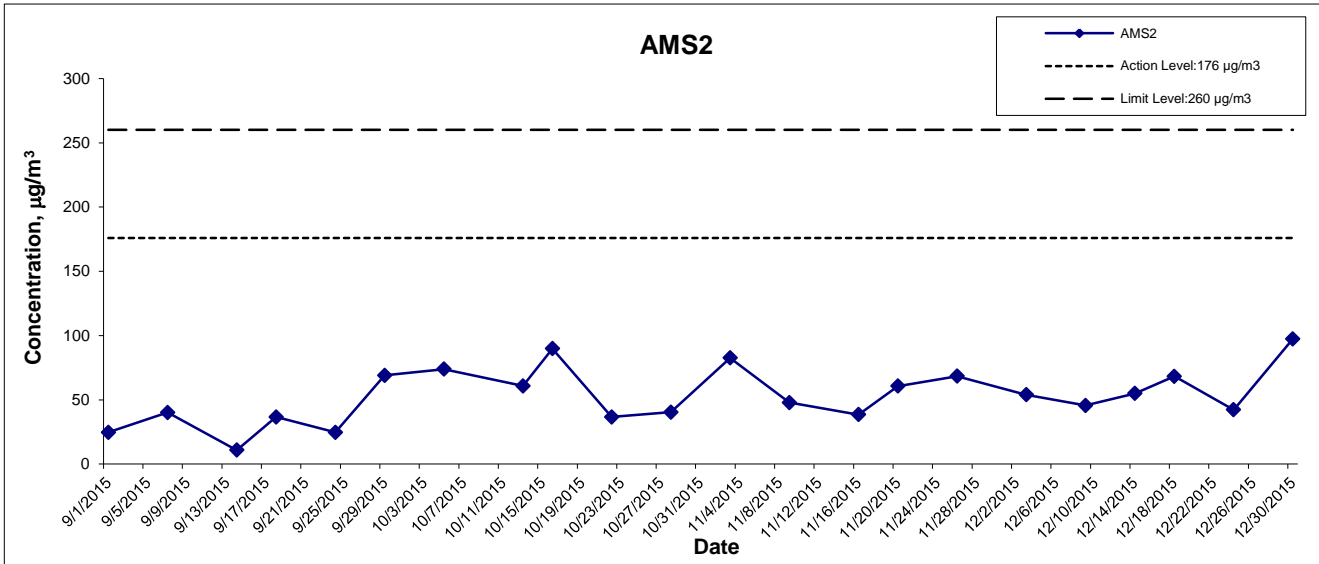

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact 24-hour TSP
 Monitoring Results



APPENDIX H Meteorological Data for Monitoring Periods on Monitoring Dates in December 2015

WIND DATA

Date	Time	Averaged Wind Speed (m/s)	Averaged Wind Direction (degrees)
12/02/15	15:13:35	0.27	90
12/02/15	16:13:35	0.42	329
12/02/15	17:13:35	0.07	125
12/02/15	18:13:35	0.24	96
12/02/15	19:13:35	0.45	89
12/02/15	20:13:35	0.28	300
12/02/15	21:13:35	0.81	208
12/02/15	22:13:35	0.22	283
12/02/15	23:13:35	0.85	316
12/03/15	00:13:35	0.01	78
12/03/15	01:13:35	0.14	66
12/03/15	02:13:35	0.03	81
12/03/15	03:13:35	0.00	55
12/03/15	04:13:35	0.31	93
12/03/15	05:13:35	0.03	85
12/03/15	06:13:35	0.01	50
12/03/15	07:13:35	0.60	92
12/03/15	08:13:35	0.13	56
12/03/15	09:13:35	0.38	354
12/03/15	10:13:35	0.07	20
12/14/15	08:58:08	0.76	266
12/14/15	09:58:08	0.57	238
12/14/15	10:58:08	2.77	240
12/14/15	11:58:08	0.17	244
12/14/15	12:28:48	0.11	184
12/14/15	13:28:48	0.06	45
12/14/15	14:28:48	0.07	46
12/14/15	15:28:48	0.55	345
12/14/15	16:28:48	0.64	10
12/14/15	17:28:48	0.10	46
12/14/15	18:28:48	0.43	11
12/14/15	19:28:48	0.34	39
12/14/15	20:28:48	0.67	29
12/14/15	21:28:48	1.04	94
12/14/15	22:28:48	1.19	111
12/14/15	23:28:48	0.36	58
12/15/15	00:28:48	0.01	118
12/15/15	01:28:48	0.01	95
12/15/15	02:28:48	0.01	45
12/15/15	03:28:48	0.01	15
12/15/15	04:28:48	0.00	46
12/15/15	05:28:48	0.08	45
12/15/15	06:28:48	0.17	38
12/15/15	07:28:48	1.08	25
12/15/15	08:28:48	0.14	319
12/15/15	09:28:48	0.01	32
12/17/15	15:28:48	1.12	77
12/17/15	16:28:48	0.04	73
12/17/15	17:28:48	0.11	73
12/17/15	18:28:48	0.21	67
12/17/15	19:28:48	1.71	111
12/17/15	20:28:48	0.50	134
12/17/15	21:28:48	2.32	121
12/17/15	22:28:48	2.07	101
12/17/15	23:28:48	1.83	123
12/18/15	00:28:48	0.08	121
12/18/15	01:28:48	0.01	138
12/18/15	02:28:48	0.01	98
12/18/15	03:28:48	0.34	74
12/18/15	04:28:48	0.01	108
12/18/15	05:28:48	0.04	87
12/18/15	06:28:48	0.14	97
12/18/15	07:28:48	0.49	109
12/18/15	08:28:48	0.13	50
12/18/15	09:28:48	0.10	105
12/18/15	10:28:48	0.08	31
12/18/15	11:28:48	0.07	101
12/18/15	12:28:48	0.06	156
12/18/15	13:28:48	0.15	151
12/18/15	14:28:48	0.07	286
12/18/15	15:28:48	0.03	175
12/18/15	16:28:48	0.32	37
12/23/15	15:28:48	0.76	66
12/23/15	16:28:48	0.15	283
12/23/15	17:28:48	0.13	149
12/23/15	18:28:48	0.55	15
12/23/15	19:28:48	0.38	116
12/23/15	20:28:48	0.28	216
12/23/15	21:28:48	0.43	10
12/23/15	22:28:48	0.10	223
12/23/15	23:28:48	0.01	288
12/24/15	00:28:48	0.01	268
12/24/15	01:28:48	0.00	193
12/24/15	02:28:48	0.01	103
12/24/15	03:28:48	0.01	103
12/24/15	04:28:48	0.14	279
12/24/15	05:28:48	0.01	263

APPENDIX H Meteorological Data for Monitoring Periods on Monitoring Dates in December 2015

WIND DATA

Date	Time	Averaged Wind Speed (m/s)	Averaged Wind Direction (degrees)
12/24/15	06:28:48	0.08	295
12/24/15	07:28:48	0.60	279
12/24/15	08:28:48	0.08	292
12/24/15	09:28:48	0.06	74
12/24/15	10:28:48	0.04	347
12/24/15	11:20:16	0.06	88
12/24/15	12:20:16	0.24	63
12/24/15	13:20:16	1.54	102
12/24/15	14:20:16	0.27	72
12/24/15	15:20:16	1.30	114
12/24/15	16:20:16	0.08	332
12/29/15	14:20:16	0.00	95
12/29/15	15:20:16	0.21	33
12/29/15	16:20:16	0.03	71
12/29/15	17:20:16	0.04	350
12/29/15	18:20:16	0.69	263
12/29/15	19:20:16	0.31	247
12/29/15	20:20:16	0.25	314
12/29/15	21:20:16	0.24	60
12/29/15	22:20:16	0.35	183
12/29/15	23:20:16	0.03	89
12/30/15	00:20:16	1.68	120
12/30/15	01:20:16	0.14	117
12/30/15	02:20:16	0.91	89
12/30/15	03:20:16	0.03	92
12/30/15	04:20:16	0.03	48
12/30/15	05:20:16	0.03	85
12/30/15	06:20:16	0.39	114
12/30/15	07:20:16	0.97	93
12/30/15	08:20:16	0.11	94
12/30/15	09:20:16	0.13	115
12/30/15	10:20:16	0.08	71
12/30/15	11:20:16	1.13	104
12/30/15	12:20:16	0.07	99
12/30/15	13:20:16	0.07	11
12/30/15	14:20:16	0.67	304
12/30/15	15:20:16	0.53	320

Remarks: Due to malfunction of the wind data monitoring equipment, wind data was not able to be obtained for monitoring event(s) conducted between 10:13:35 3 Dec 2015 – 16:00:00 9 December 2015. Wind speed and direction dataset 10:13:35 3 Dec 2015 – 16:00:00 9 December 2015 from the Hong Kong Observatory is not available at time this monthly report is submitted.

Appendix I Impact Daytime Construction Noise Monitoring Results

Daytime Noise Monitoring Results at Station NMS2 - Seaview Crescent Tower 1

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Averaged Wind Speed (m/s)	Baseline Noise Level, dB(A)	Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq				
03-Dec-15	Fine	10:30	64	69	68	<5m/s	62.9	75	N
09-Dec-15	Fine	10:45	63	68	65	<5m/s	62.9	75	N
14-Dec-15	Cloudy	10:46	63	64	63	<5m/s	62.9	75	N
24-Dec-15	Fine	13:50	65	69	67	<5m/s	62.9	75	N
30-Dec-15	Fine	10:40	63	72	68	<5m/s	62.9	75	N
		Min	63	64	63				
		Max	65	72	68				
		Average	--	--	67				

Daytime Noise Monitoring Results at Station NMS3B - Site Boundary of Site Office (WA2)

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Averaged Wind Speed (m/s)	Baseline Noise Level, dB(A) ^	Limit Level, dB(A)**	Exceedance (Y/N)
		Time	L90	L10	Leq				
03-Dec-15	Fine	11:15	64	69	66	<5m/s	66.3	70	N
09-Dec-15	Fine	13:14	65	69	67	<5m/s	66.3	70	N
14-Dec-15	Cloudy	11:46	64	69	67	<5m/s	66.3	70	N
24-Dec-15	Fine	13:02	61	67	64	<5m/s	66.3	70	N
30-Dec-15	Fine	09:50	57	73	68	<5m/s	66.3	70	N
		Min	57	67	64				
		Max	65	73	68				
		Average	--	--	67				



Remark:

[#] A correction of +3dB(A) was made to the free field measurement.

* Façade measurement.

^ Averaged baseline noise level recorded at NMS3 Ho Yu College is adopted.

** Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school examination period.

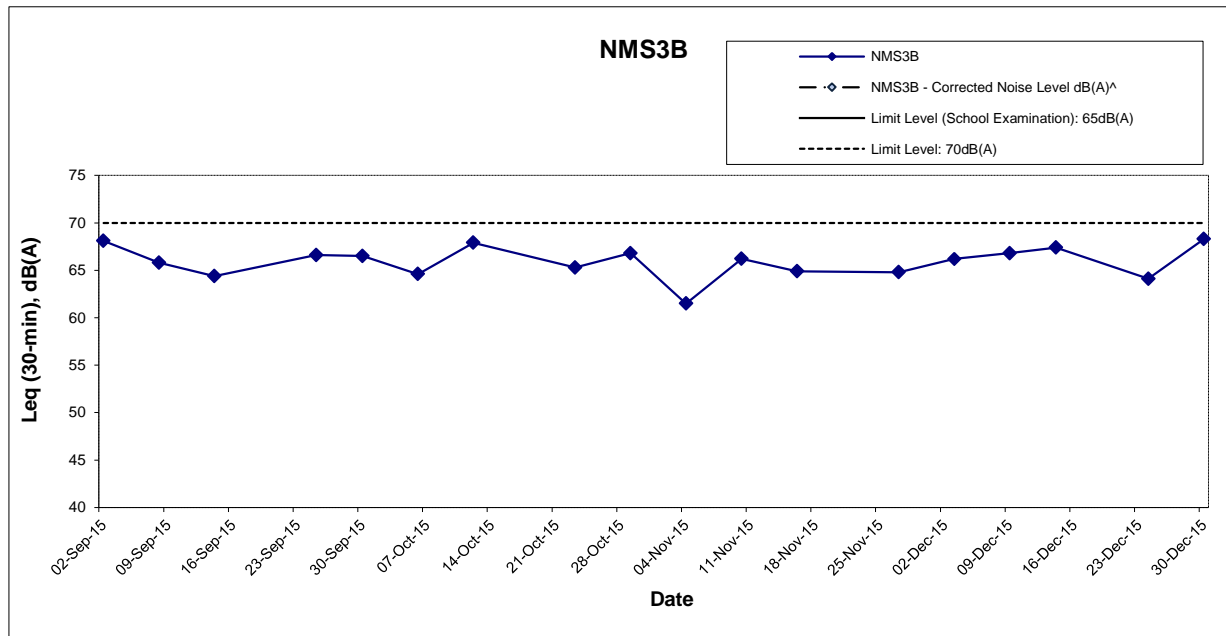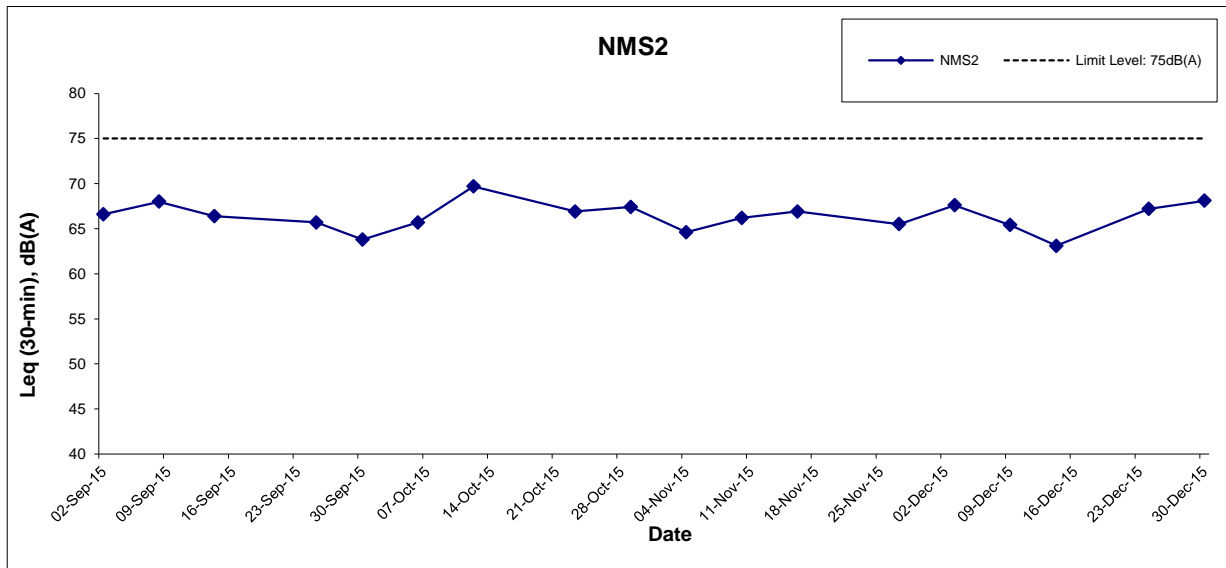

Remarks: Effective from July 2012, the Limit Level at NMS3A was revised to 70dB(A). Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Daytime
 Construction Noise Monitoring Results



Project No.: 60249820

Date: Jan 2016

Appendix I

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:03	6.5	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	26.9 25.6	26.2	92.3 92.2	92.3	7.2 7.1	7.1	7.1	4.3 4.5	4.4	4.6	5.8 6.2	6.0	5.4
					Middle	3.3	20.3 20.3	20.3	8.1 8.1	8.1	28.6 27.0	27.8	92.7 91.3	92.0	7.1 7.1	7.1		4.4 4.6	4.5		4.0 4.1	4.1	
					Bottom	5.5	20.3 20.3	20.3	8.1 8.1	8.1	28.9 28.8	28.9	92.4 91.7	92.1	7.1 7.0	7.0		4.7 4.8	4.8		5.6 6.3	6.0	
4-Dec-15	Cloudy	Moderate	06:27	6.3	Surface	1.0	19.8 19.8	19.8	8.1 8.1	8.1	28.2 27.6	27.9	92.4 93.3	92.9	7.1 7.2	7.2	7.2	3.2 3.1	3.2	3.4	4.6 4.0	4.3	4.5
					Middle	3.2	19.8 19.9	19.9	8.1 8.1	8.1	28.0 28.7	28.3	94.3 92.5	93.4	7.2 7.1	7.1		3.3 3.4	3.4		4.9 4.9	4.9	
					Bottom	5.3	20.1 20.0	20.0	8.1 8.1	8.1	30.5 28.6	29.6	91.4 92.4	91.9	7.1 7.1	7.1		3.5 3.6	3.6		4.7 3.7	4.2	
7-Dec-15	Cloudy	Moderate	11:01	6.3	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	32.5 33.2	32.9	93.8 92.6	93.2	7.1 7.0	7.1	7.1	6.1 6.0	6.1	6.3	5.9 5.6	5.8	6.1
					Middle	3.2	19.5 19.4	19.4	8.2 8.2	8.2	32.6 33.8	33.2	93.1 92.1	92.6	7.0 7.0	7.0		6.3 6.2	6.3		5.2 6.4	5.8	
					Bottom	5.3	19.4 19.4	19.4	8.2 8.2	8.2	34.2 33.0	33.6	91.7 93.2	92.5	7.0 7.1	7.0		6.4 6.5	6.5		7.4 5.7	6.6	
9-Dec-15	Rainy	Moderate	11:42	7.0	Surface	1.0	18.1 18.1	18.1	8.2 8.2	8.2	30.3 30.6	30.5	103.4 95.4	99.4	8.1 7.5	7.8	7.7	9.4 9.3	9.4	9.5	3.5 3.0	3.3	3.0
					Middle	3.5	18.1 18.1	18.1	8.2 8.2	8.2	30.8 30.6	30.7	95.0 98.5	96.8	7.5 7.8	7.6		9.4 9.6	9.5		3.2 2.3	2.8	
					Bottom	6.0	18.1 18.1	18.1	8.2 8.2	8.2	30.8 30.8	30.8	94.2 95.2	94.7	7.4 7.5	7.5		9.5 9.6	9.6		2.4 3.4	2.9	
11-Dec-15	Sunny	Moderate	12:26	6.3	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	27.6 27.9	27.7	94.8 93.7	94.3	7.5 7.5	7.5	7.5	5.6 5.7	5.7	6.2	5.4 4.7	5.1	5.0
					Middle	3.2	18.2 18.2	18.2	8.2 8.2	8.2	29.5 29.7	29.6	94.3 92.9	93.6	7.4 7.3	7.4		6.5 6.3	6.4		4.5 4.1	4.3	
					Bottom	5.3	18.2 18.2	18.2	8.2 8.2	8.2	30.1 30.2	30.1	93.0 93.0	93.0	7.4 7.3	7.3		6.4 6.3	6.4		5.5 5.9	5.7	
14-Dec-15	Rainy	Moderate	14:22	6.5	Surface	1.0	17.9 17.9	17.9	8.1 8.1	8.1	21.0 21.0	21.0	91.5 92.5	92.0	7.6 7.6	7.6	7.6	5.3 5.2	5.3	5.5	7.5 7.8	7.7	7.4
					Middle	3.3	18.1 18.0	18.0	8.1 8.1	8.1	25.2 21.6	23.4	92.2 91.5	91.9	7.5 7.5	7.5		5.4 5.5	5.5		6.7 7.1	6.9	
					Bottom	5.5	18.1 18.1	18.1	8.1 8.1	8.1	27.2 27.2	27.2	91.2 91.3	91.3	7.4 7.4	7.4		5.7 5.8	5.8		7.3 8.0	7.7	
16-Dec-15	Sunny	Moderate	16:11	6.4	Surface	1.0	17.3 17.4	17.4	8.2 8.2	8.2	27.2 27.5	27.4	94.0 92.2	93.1	7.7 7.5	7.6	7.6	6.7 6.6	6.7	6.7	7.8 7.9	7.9	9.0
					Middle	3.2	17.5 17.5	17.5	8.2 8.2	8.2	27.8 27.9	27.9	93.7 92.6	93.2	7.6 7.5	7.5		6.7 6.8	6.8		8.9 8.6	8.8	
					Bottom	5.4	17.6 17.5	17.5	8.2 8.2	8.2	28.2 27.8	28.0	92.0 93.0	92.5	7.4 7.5	7.5		6.8 6.6	6.7		10.0 10.3	10.2	
18-Dec-15	Sunny	Moderate	12:22	6.4	Surface	1.0	15.9 15.9	15.9	8.2 8.2	8.2	28.8 28.8	28.8	95.8 95.7	95.8	8.0 7.9	7.9	7.9	7.1 7.1	7.1	7.4	7.7 7.7	7.7	8.0
					Middle	3.2	15.9 15.9	15.9	8.2 8.2	8.2	29.0 28.8	28.9	95.4 95.5	95.5	7.9 7.9	7.9		7.4 7.6	7.5		8.1 7.5	7.8	
					Bottom	5.4	15.9 15.9	15.9	8.2 8.2	8.2	29.1 28.9	29.0	95.3 95.2	95.3	7.9 7.9	7.9		7.3 7.6	7.5		8.5 8.6	8.6	
21-Dec-15	Cloudy	Moderate	09:28	6.4	Surface	1.0	15.8 15.9	15.8	8.1 8.1	8.1	30.1 29.4	29.8	94.4 96.0	95.2	7.8 7.9	7.9	7.9	3.5 3.5	3.5	3.5	4.7 3.6	4.2	4.1
					Middle	3.2	16.1 15.9	16.0	8.1 8.1	8.1	30.7 30.6	30.6	96.2 95.7	96.0	7.9 7.9	7.9		3.6 3.5	3.6		3.6 3.1	3.4	
					Bottom	5.4	16.0 16.2	16.1	8.1 8.1	8.1	31.1 32.4	31.8	96.2 99.0	97.6	7.9 8.0	7.9		3.5 3.5	3.5		5.2 4.4	4.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	11:28	6.7	Surface	1.0	16.3 16.3	16.3	8.1 8.1	8.1	24.3 24.6	24.4	95.2 95.6	95.4	8.1 8.1	8.1	8.1	5.4 5.2	5.3	5.7	3.1 4.8	4.0	4.9
					Middle	3.4	16.2 16.2	16.2	8.1 8.1	8.1	27.1 26.7	26.9	95.6 95.0	95.3	8.0 7.9	8.0		5.7 5.7	5.7		4.1 4.7	4.4	
					Bottom	5.7	16.3 16.3	16.3	8.1 8.1	8.1	28.1 28.9	28.5	95.2 95.8	95.5	7.9 8.0	7.9		5.9 6.1	6.0		5.3 7.1	6.2	
25-Dec-15	Cloudy	Moderate	12:11	7.1	Surface	1.0	16.6 16.6	16.6	8.1 8.1	8.1	22.9 23.1	23.0	94.0 94.3	94.2	7.9 7.9	7.9	7.9	7.5 7.6	7.6	7.6	8.9 9.4	9.2	9.2
					Middle	3.6	16.6 16.7	16.7	8.1 8.1	8.1	24.3 24.4	24.3	92.8 92.9	92.9	7.9 7.9	7.9		7.5 7.6	7.6		8.4 9.5	9.0	
					Bottom	6.1	16.7 16.7	16.7	8.1 8.0	8.1	24.9 24.9	24.9	92.8 92.8	92.8	7.8 7.8	7.8		7.7 7.6	7.7		9.5 9.4	9.5	
28-Dec-15	Sunny	Moderate	14:17	6.5	Surface	1.0	15.9 16.0	15.9	8.2 8.2	8.2	27.2 27.3	27.2	95.3 95.1	95.2	8.0 8.0	8.0	8.0	6.5 6.6	6.6	6.7	8.8 8.6	8.7	8.4
					Middle	3.3	16.0 16.0	16.0	8.1 8.2	8.2	27.5 27.2	27.4	94.9 95.2	95.1	7.9 8.0	8.0		6.7 6.7	6.7		8.6 8.1	8.4	
					Bottom	5.5	16.0 16.0	16.0	8.2 8.1	8.1	27.3 28.1	27.7	94.9 94.9	94.9	7.9 7.9	7.9		6.9 6.9	6.9		8.6 7.5	8.1	
30-Dec-15	Cloudy	Moderate	15:47	6.4	Surface	1.0	16.0 16.1	16.1	8.2 8.2	8.2	26.9 27.1	27.0	96.9 94.2	95.6	8.1 7.9	8.0	8.0	3.8 3.9	3.9	4.1	2.9 3.1	3.0	3.5
					Middle	3.2	16.0 16.0	16.0	8.2 8.2	8.2	27.3 27.3	27.3	94.0 96.7	95.4	7.9 8.1	8.0		4.1 3.9	4.0		2.9 3.6	3.3	
					Bottom	5.4	16.0 16.0	16.0	8.2 8.2	8.2	27.7 27.9	27.8	96.3 95.6	96.0	8.0 8.0	8.0		4.2 4.4	4.3		5.0 3.2	4.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	13:04	6.6	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	26.8 27.8	27.3	95.0 95.4	95.2	7.3 7.3	7.3	7.3	5.0 4.9	5.0	5.3	6.1 5.7	5.9	6.2
					Middle	3.3	20.4 20.4	20.4	8.1 8.1	8.1	28.6 27.7	28.1	95.4 94.6	95.0	7.2 7.2	7.2		5.2 5.3	5.3		6.4 6.4	6.4	
					Bottom	5.6	20.4 20.4	20.4	8.1 8.1	8.1	29.7 28.3	29.0	93.3 92.8	93.1	7.1 7.1	7.1		5.5 5.4	5.5		6.3 6.5	6.4	
4-Dec-15	Cloudy	Moderate	14:36	6.5	Surface	1.0	19.6 19.6	19.6	8.2 8.2	8.2	25.6 25.8	25.7	91.2 92.9	92.1	7.2 7.1	7.1	7.1	3.3 3.4	3.4	3.6	2.6 3.7	3.2	3.5
					Middle	3.3	20.0 20.3	20.1	8.2 8.2	8.2	27.2 26.9	27.0	90.6 91.9	91.3	7.1 7.0	7.1		3.5 3.6	3.6		2.8 3.8	3.3	
					Bottom	5.5	20.3 20.1	20.2	8.2 8.2	8.2	29.1 28.7	28.9	90.1 89.8	90.0	7.0 7.0	7.0		3.9 3.8	3.9		4.0 4.0	4.0	
7-Dec-15	Cloudy	Moderate	16:22	6.5	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	32.8 33.2	33.0	93.7 93.5	93.6	7.1 7.1	7.1	7.1	3.3 3.4	3.4	3.6	6.1 6.2	6.2	5.8
					Middle	3.3	19.4 19.4	19.4	8.2 8.2	8.2	33.0 33.4	33.2	92.2 92.0	92.1	7.0 7.0	7.0		3.5 3.6	3.6		5.9 6.0	6.0	
					Bottom	5.5	19.4 19.4	19.4	8.2 8.2	8.2	33.8 33.2	33.5	91.5 91.7	91.6	6.9 6.9	6.9		3.9 3.8	3.9		5.4 5.1	5.3	
9-Dec-15	Rainy	Moderate	16:25	7.1	Surface	1.0	18.0 18.0	18.0	8.2 8.2	8.2	31.6 31.2	31.4	95.6 96.4	96.0	7.5 7.6	7.5	7.5	7.3 7.4	7.4	7.5	4.0 4.9	4.5	4.7
					Middle	3.6	18.1 18.1	18.1	8.2 8.2	8.2	31.8 31.4	31.6	95.4 95.5	95.5	7.5 7.5	7.5		7.6 7.5	7.6		3.9 4.8	4.4	
					Bottom	6.1	18.1 18.1	18.1	8.2 8.2	8.2	31.5 32.2	31.8	95.1 95.4	95.3	7.5 7.5	7.5		7.5 7.6	7.6		4.2 6.1	5.2	
11-Dec-15	Sunny	Moderate	07:50	6.5	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	30.3 31.0	30.7	95.6 98.0	96.8	7.5 7.6	7.6	7.6	11.1 11.2	11.2	11.3	12.3 11.9	12.1	12.3
					Middle	3.3	18.2 18.2	18.2	8.2 8.2	8.2	31.5 30.6	31.1	95.9 95.4	95.7	7.5 7.5	7.5		11.3 11.2	11.3		12.5 12.5	12.5	
					Bottom	5.5	18.2 18.2	18.2	8.2 8.2	8.2	31.0 32.5	31.7	95.1 96.0	95.6	7.5 7.5	7.5		11.4 11.5	11.5		12.2 12.3	12.3	
14-Dec-15	Rainy	Moderate	10:12	6.6	Surface	1.0	18.0 18.0	18.0	8.1 8.1	8.1	25.3 26.0	25.7	96.3 96.6	96.5	7.8 7.8	7.8	7.8	6.2 6.1	6.2	6.3	6.7 5.9	6.3	6.9
					Middle	3.3	18.1 18.1	18.1	8.1 8.1	8.1	26.4 25.7	26.0	95.4 95.2	95.3	7.7 7.7	7.7		6.2 6.4	6.3		6.7 6.4	6.6	
					Bottom	5.6	18.1 18.1	18.1	8.1 8.1	8.1	29.0 27.6	28.3	93.2 93.7	93.5	7.6 7.6	7.6		6.5 6.5	6.5		7.0 8.6	7.8	
16-Dec-15	Sunny	Moderate	11:30	6.4	Surface	1.0	17.4 17.4	17.4	8.1 8.1	8.1	28.2 27.5	27.8	98.3 96.3	97.3	7.9 7.8	7.8	7.8	16.7 16.2	16.5	16.4	14.2 14.0	14.1	17.4
					Middle	3.2	17.4 17.4	17.4	8.1 8.1	8.1	29.1 27.7	28.4	96.9 93.7	95.3	7.8 7.6	7.7		16.5 16.1	16.3		17.4 19.1	18.3	
					Bottom	5.4	17.4 17.5	17.5	8.1 8.1	8.1	28.1 29.6	28.8	93.4 96.5	95.0	7.6 7.8	7.7		16.4 16.3	16.4		20.6 19.2	19.9	
18-Dec-15	Cloudy	Moderate	05:55	6.3	Surface	1.0	16.6 16.6	16.6	8.1 8.1	8.1	29.1 28.8	29.0	101.6 99.4	100.5	8.3 8.1	8.2	8.3	6.7 6.3	6.5	6.5	5.1 6.1	5.6	4.8
					Middle	3.2	16.6 16.5	16.5	8.1 8.1	8.1	29.3 29.0	29.1	101.4 103.0	102.2	8.3 8.4	8.4		6.2 6.5	6.4		4.2 3.9	4.1	
					Bottom	5.3	16.5 16.4	16.5	8.1 8.1	8.1	29.0 29.3	29.2	105.5 111.1	108.3	8.6 9.1	8.9		6.6 6.4	6.5		4.4 5.0	4.7	
21-Dec-15	Sunny	Moderate	14:55	6.4	Surface	1.0	16.3 16.3	16.3	8.2 8.2	8.2	30.9 30.6	30.8	95.2 96.8	96.0	7.8 7.9	7.8	7.8	3.0 3.0	3.0	3.3	3.7 3.1	3.4	3.1
					Middle	3.2	16.0 16.2	16.1	8.2 8.2	8.2	31.0 30.7	30.9	95.1 96.3	95.7	7.7 7.9	7.8		3.6 3.4	3.5		3.2 2.6	2.9	
					Bottom	5.4	16.1 16.0	16.1	8.2 8.2	8.2	30.9 31.4	31.1	96.1 93.7	94.9	7.8 7.7	7.7		3.4 3.5	3.5		3.0 2.9	3.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	16:54	6.7	Surface	1.0	16.6 16.7	16.7	8.1 8.1	8.1	25.0 25.0	25.0	95.4 95.5	95.5	7.9 8.0	7.9	7.9	5.3 5.3	5.3	5.6	3.9 3.0	3.5	3.7
					Middle	3.4	16.4 16.3	16.3	8.1 8.1	8.1	25.5 26.2	25.8	95.1 94.3	94.7	7.9 7.9	7.9		5.6 5.5	5.6		4.3 3.0	3.7	
					Bottom	5.7	16.4 16.3	16.4	8.1 8.1	8.1	27.8 28.1	27.9	94.6 93.1	93.9	7.9 7.8	7.8		5.8 5.9	5.9		4.3 4.3	3.9	
25-Dec-15	Cloudy	Moderate	07:58	7.3	Surface	1.0	16.7 16.7	16.7	8.0 8.0	8.0	26.8 28.1	27.5	99.6 106.4	103.0	8.2 8.6	8.4	8.4	7.8 7.8	7.8	7.9	9.8 9.1	9.5	9.5
					Middle	3.7	16.7 16.7	16.7	8.0 8.0	8.0	28.9 27.3	28.1	103.1 98.8	101.0	8.4 8.2	8.3		8.0 7.9	8.0		9.1 8.8	9.0	
					Bottom	6.3	16.7 16.7	16.7	8.0 8.0	8.0	27.6 29.9	28.8	97.1 101.6	99.4	8.0 8.3	8.2		8.0 8.0	8.0		9.9 10.0	10.0	
28-Dec-15	Sunny	Moderate	10:10	6.6	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	26.0 25.8	25.9	95.8 95.7	95.8	8.1 8.1	8.1	8.1	19.8 19.8	19.8	20.2	18.7 18.8	18.8	18.7
					Middle	3.3	16.0 16.0	16.0	8.1 8.1	8.1	25.9 26.2	26.1	95.2 95.4	95.3	8.0 8.1	8.0		20.2 20.2	20.2		18.8 18.9	18.9	
					Bottom	5.6	16.0 16.0	16.0	8.1 8.1	8.1	26.2 26.0	26.1	94.9 94.2	94.6	8.0 8.0	8.0		20.5 20.6	20.6		18.3 18.3	18.3	
30-Dec-15	Cloudy	Moderate	11:22	6.5	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	28.6 28.2	28.4	96.0 94.3	95.2	8.0 7.9	7.9	8.0	6.8 6.9	6.9	7.1	9.4 7.8	8.6	8.3
					Middle	3.3	16.0 16.0	16.0	8.1 8.1	8.1	29.0 28.4	28.7	96.3 95.4	95.9	8.0 7.9	8.0		7.1 7.3	7.2		8.3 7.6	8.0	
					Bottom	5.5	16.0 16.0	16.0	8.1 8.1	8.1	28.5 29.7	29.1	97.0 97.9	97.5	8.1 8.1	8.1		6.9 7.4	7.2		9.1 7.4	8.3	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	16:53	15.7	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	26.8 25.7	26.2	93.2 93.5	93.4	7.1 7.1	7.1	7.1	4.9 4.9	4.9	5.2	5.3 5.1	5.2	5.9
					Middle	7.9	20.3 20.3	20.3	8.2 8.2	8.2	29.0 29.9	29.4	92.7 92.8	92.8	7.0 7.0	7.0		5.1 5.2	5.2		6.7 6.7	6.7	
					Bottom	14.7	20.3 20.3	20.3	8.2 8.2	8.2	29.9 29.9	29.9	92.5 91.8	92.2	7.0 7.0	7.0		5.4 5.4	5.4		5.9 5.9	5.9	
4-Dec-15	Cloudy	Moderate	06:49	15.2	Surface	1.0	19.8 19.8	19.8	8.1 8.1	8.1	26.9 27.1	27.0	92.6 92.7	92.7	7.2 7.2	7.2	7.2	3.1 3.2	3.2	3.4	3.1 3.2	3.2	3.5
					Middle	7.6	19.9 19.8	19.9	8.1 8.1	8.1	26.9 27.5	27.2	90.1 91.8	91.0	7.0 7.1	7.1		3.4 3.3	3.4		3.6 3.3	3.5	
					Bottom	14.2	20.0 20.1	20.0	8.1 8.1	8.1	27.8 28.5	28.2	91.2 91.3	91.3	7.1 7.0	7.0		3.5 3.6	3.6		3.5 3.9	3.7	
7-Dec-15	Cloudy	Moderate	11:23	15.3	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	31.8 31.8	31.8	90.6 91.2	90.9	6.9 6.9	6.9	6.9	5.3 5.4	5.4	5.6	8.8 8.7	8.8	8.6
					Middle	7.7	19.5 19.5	19.5	8.2 8.2	8.2	31.9 31.9	31.9	90.2 90.2	90.2	6.9 6.9	6.9		5.5 5.6	5.6		9.1 7.9	8.5	
					Bottom	14.3	19.5 19.5	19.5	8.2 8.2	8.2	32.1 31.9	32.0	89.9 89.1	89.5	6.9 6.8	6.8		5.7 5.7	5.7		8.9 8.0	8.5	
9-Dec-15	Rainy	Moderate	12:06	18.1	Surface	1.0	18.1 18.1	18.1	8.2 8.2	8.2	29.9 29.9	29.9	95.0 93.7	94.4	7.5 7.4	7.5	7.5	9.2 9.4	9.3	9.5	7.5 7.5	7.5	8.5
					Middle	9.1	18.1 18.1	18.1	8.2 8.2	8.2	29.9 30.0	30.0	94.4 93.7	94.1	7.5 7.4	7.4		9.5 9.4	9.5		8.7 8.5	8.6	
					Bottom	17.1	18.1 18.1	18.1	8.2 8.2	8.2	30.1 29.9	30.0	93.6 93.7	93.7	7.4 7.4	7.4		9.5 9.7	9.6		9.4 9.4	9.4	
11-Dec-15	Sunny	Moderate	12:00	16.1	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	28.7 28.0	28.4	93.5 94.3	93.9	7.4 7.4	7.4	7.4	6.1 6.2	6.2	7.3	5.0 5.1	5.1	4.6
					Middle	8.1	18.2 18.2	18.2	8.2 8.2	8.2	31.5 30.9	31.2	93.1 93.4	93.3	7.3 7.3	7.3		7.8 7.9	7.9		3.8 5.4	4.6	
					Bottom	15.1	18.2 18.2	18.2	8.2 8.2	8.2	31.7 31.0	31.4	92.7 92.7	92.7	7.2 7.3	7.3		7.8 7.8	7.8		3.8 4.5	4.2	
14-Dec-15	Rainy	Moderate	14:02	16.2	Surface	1.0	17.9 18.0	17.9	8.1 8.1	8.1	21.8 22.5	22.1	93.9 93.8	93.9	7.6 7.7	7.6	7.6	6.2 5.8	6.0	6.3	7.3 7.5	7.4	7.7
					Middle	8.1	18.1 18.0	18.1	8.1 8.1	8.1	24.1 27.6	25.9	93.3 92.1	92.7	7.5 7.5	7.5		6.4 6.2	6.3		7.5 7.4	7.5	
					Bottom	15.2	18.0 17.9	17.9	8.1 8.1	8.1	28.1 23.2	25.6	92.6 91.9	92.3	7.5 7.5	7.5		6.6 6.4	6.5		7.7 8.8	8.3	
16-Dec-15	Sunny	Moderate	15:50	16.3	Surface	1.0	17.4 17.4	17.4	8.2 8.2	8.2	28.8 27.9	28.3	95.2 93.9	94.6	7.6 7.5	7.6	7.5	6.5 6.5	6.5	6.6	6.8 6.5	6.7	7.5
					Middle	8.2	17.6 17.6	17.6	8.2 8.2	8.2	29.6 28.9	29.2	91.7 92.8	92.3	7.4 7.5	7.4		6.5 6.7	6.6		6.4 7.0	6.7	
					Bottom	15.3	17.5 17.7	17.6	8.2 8.2	8.2	29.2 30.3	29.8	91.7 91.6	91.7	7.4 7.3	7.4		6.7 6.5	6.6		9.1 8.8	9.0	
18-Dec-15	Sunny	Moderate	12:04	16.4	Surface	1.0	15.9 15.9	15.9	8.2 8.2	8.2	29.2 29.4	29.3	96.4 95.8	96.1	8.0 7.9	8.0	8.0	9.8 9.1	9.5	10.9	7.0 7.7	7.4	7.2
					Middle	8.2	15.9 15.9	15.9	8.2 8.2	8.2	29.2 29.5	29.4	96.4 97.7	97.1	8.0 8.1	8.0		10.9 11.5	11.2		7.2 7.1	7.2	
					Bottom	15.4	15.9 15.9	15.9	8.2 8.2	8.2	29.3 29.7	29.5	95.9 97.8	96.9	7.9 8.1	8.0		12.0 12.2	12.1		6.9 7.1	7.0	
21-Dec-15	Cloudy	Moderate	09:51	16.4	Surface	1.0	15.9 16.0	15.9	8.2 8.2	8.2	29.5 28.9	29.2	95.0 95.9	95.5	7.8 7.8	7.8	7.8	6.5 6.8	6.7	6.7	5.0 5.1	5.1	4.0
					Middle	8.2	16.2 16.2	16.2	8.1 8.1	8.1	30.5 30.5	30.5	94.8 95.0	94.9	7.8 7.8	7.8		6.6 6.8	6.7		4.0 3.5	3.8	
					Bottom	15.4	16.1 16.2	16.1	8.1 8.1	8.1	30.5 30.5	30.5	94.5 93.1	93.8	7.8 7.7	7.7		6.7 6.6	6.7		2.2 3.8	3.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	11:50	15.4	Surface	1.0	16.3 16.4	16.4	8.1 8.1	8.1	24.1 24.0	24.1	95.2 93.8	94.5	8.1 7.9	8.0	8.0	3.6 3.4	3.5	3.8	4.8 3.1	4.0	3.7
					Middle	7.7	16.3 16.3	16.3	8.1 8.1	8.1	24.6 24.9	24.7	93.5 94.8	94.2	7.9 8.0	8.0		3.7 3.8	3.8		4.2 3.6	3.9	
					Bottom	14.4	16.3 16.3	16.3	8.1 8.1	8.1	27.3 27.5	27.4	94.6 94.8	94.7	7.9 7.9	7.9		4.2 4.1	4.2		3.6 2.9	3.3	
25-Dec-15	Cloudy	Moderate	11:55	18.0	Surface	1.0	16.5 16.6	16.6	8.1 8.1	8.1	23.1 23.1	23.1	95.3 95.0	95.2	8.0 8.0	8.0	8.0	7.6 7.6	7.6	7.7	8.0 8.7	8.4	7.9
					Middle	9.0	16.6 16.7	16.7	8.0 8.1	8.1	24.4 24.7	24.6	94.8 94.9	94.9	8.0 8.0	8.0		7.6 7.7	7.7		7.6 7.0	7.3	
					Bottom	17.0	16.7 16.7	16.7	8.0 8.0	8.0	25.3 25.1	25.2	94.2 94.7	94.5	8.0 7.9	8.0		7.8 7.7	7.8		7.3 8.7	8.0	
28-Dec-15	Sunny	Moderate	13:57	15.7	Surface	1.0	16.0 16.0	16.0	8.2 8.2	8.2	28.3 28.2	28.3	96.4 97.2	96.8	8.0 8.0	8.0	8.0	7.6 7.5	7.6	7.7	9.7 9.6	9.7	9.2
					Middle	7.9	16.0 16.0	16.0	8.1 8.2	8.2	28.5 28.2	28.4	96.3 96.3	96.3	8.0 8.0	8.0		7.7 7.7	7.7		9.7 9.1	9.4	
					Bottom	14.7	16.0 16.0	16.0	8.2 8.1	8.2	28.1 29.0	28.6	96.0 96.0	96.0	8.0 8.0	8.0		7.8 7.8	7.8		8.7 8.0	8.4	
30-Dec-15	Cloudy	Moderate	15:22	16.2	Surface	1.0	16.1 16.1	16.1	8.2 8.2	8.2	27.7 28.1	27.9	95.7 96.9	96.3	8.0 8.1	8.0	7.9	4.0 3.9	4.0	4.3	3.8 3.2	3.5	3.1
					Middle	8.1	16.0 16.0	16.0	8.2 8.2	8.2	28.5 29.4	29.0	93.6 93.1	93.4	7.8 7.7	7.7		4.3 4.4	4.4		2.8 2.5	2.7	
					Bottom	15.2	16.0 16.0	16.0	8.2 8.2	8.2	29.6 28.7	29.2	96.3 96.6	96.5	7.9 8.0	8.0		4.5 4.3	4.4		3.0 3.2	3.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Dec-15	Sunny	Moderate	13:26	15.8	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	26.2 26.4	26.3	94.5 93.8	94.2	7.3 7.2	7.3	4.2 4.1	4.2	4.5	4.2 3.8	4.0	4.2
					Middle	7.9	20.4 20.4	20.4	8.1 8.1	8.1	27.1 26.1	26.6	92.8 94.7	93.8	7.2 7.3	7.2	4.4 4.5	4.5		4.6 4.5	4.6	
					Bottom	14.8	20.4 20.4	20.4	8.0 8.1	8.1	27.9 27.2	27.6	92.8 92.7	92.8	7.2 7.1	7.2	4.6 4.7	4.7		4.0 4.1	4.1	
4-Dec-15	Cloudy	Moderate	14:15	15.2	Surface	1.0	19.4 19.5	19.5	8.2 8.2	8.2	27.0 26.4	26.7	92.0 91.7	91.9	7.0 7.1	7.1	3.6 3.7	3.7	3.9	4.8 4.7	4.8	4.1
					Middle	7.6	20.3 20.2	20.3	8.2 8.2	8.2	30.4 28.8	29.6	93.3 90.6	92.0	7.0 7.0	7.0	3.7 3.9	3.8		3.1 3.6	3.4	
					Bottom	14.2	20.4 20.2	20.3	8.2 8.2	8.2	32.2 30.5	31.3	90.0 89.9	90.0	6.8 6.9	6.9	4.2 4.3	4.3		4.0 4.3	4.2	
7-Dec-15	Cloudy	Moderate	16:01	15.5	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	34.1 35.0	34.6	93.9 93.3	93.6	7.0 7.0	7.0	4.0 4.0	4.0	4.1	4.4 5.2	4.8	4.6
					Middle	7.8	19.4 19.4	19.4	8.2 8.2	8.2	35.0 34.5	34.8	92.5 93.2	92.9	6.9 6.9	6.9	4.1 4.1	4.1		4.8 4.6	4.7	
					Bottom	14.5	19.5 19.4	19.4	8.2 8.2	8.2	34.8 35.1	35.0	92.0 91.9	92.0	6.9 6.9	6.9	4.3 4.2	4.3		5.0 3.6	4.3	
9-Dec-15	Rainy	Moderate	16:08	18.2	Surface	1.0	18.0 18.0	18.0	8.1 8.2	8.2	33.1 32.4	32.8	95.6 95.7	95.7	7.4 7.5	7.4	7.2 7.4	7.3	7.5	2.5 2.2	2.4	3.5
					Middle	9.1	18.0 18.1	18.1	8.1 8.1	8.1	32.7 33.3	33.0	95.6 95.4	95.5	7.4 7.4	7.4	7.6 7.5	7.6		4.3 4.5	4.4	
					Bottom	17.2	18.1 18.0	18.1	8.1 8.1	8.1	33.6 32.9	33.2	95.3 95.3	95.3	7.4 7.4	7.4	7.7 7.6	7.7		3.1 4.0	3.6	
11-Dec-15	Sunny	Moderate	08:16	16.5	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	29.6 29.5	29.5	94.7 94.1	94.4	7.5 7.4	7.4	12.2 11.9	12.1	14.3	12.8 12.2	12.5	12.5
					Middle	8.3	18.2 18.2	18.2	8.2 8.2	8.2	29.8 29.7	29.7	93.2 94.1	93.7	7.4 7.4	7.4	15.8 15.1	15.5		12.1 11.6	11.9	
					Bottom	15.5	18.2 18.2	18.2	8.2 8.2	8.2	29.8 29.9	29.9	92.4 92.8	92.6	7.3 7.3	7.3	15.2 15.3	15.3		13.8 12.6	13.2	
14-Dec-15	Rainy	Moderate	10:34	16.3	Surface	1.0	18.0 18.0	18.0	8.1 8.1	8.1	24.9 24.4	24.7	92.9 92.8	92.9	7.5 7.6	7.5	5.2 5.3	5.3	5.5	7.9 8.0	8.0	7.5
					Middle	8.2	18.0 18.1	18.1	8.1 8.1	8.1	24.6 25.4	25.0	91.7 92.1	91.9	7.5 7.5	7.5	5.4 5.5	5.5		7.3 6.2	6.8	
					Bottom	15.3	18.1 18.1	18.1	8.1 8.1	8.1	25.1 27.0	26.0	91.3 92.2	91.8	7.4 7.5	7.5	5.7 5.8	5.8		7.0 8.3	7.7	
16-Dec-15	Sunny	Moderate	11:51	16.5	Surface	1.0	17.4 17.5	17.4	8.1 8.1	8.1	27.0 27.1	27.1	93.6 94.2	93.9	7.6 7.7	7.6	16.2 16.1	16.2	16.4	16.1 17.8	17.0	17.0
					Middle	8.3	17.5 17.5	17.5	8.1 8.1	8.1	27.2 27.2	27.2	92.7 92.5	92.6	7.5 7.5	7.5	16.2 16.5	16.4		16.8 18.4	17.6	
					Bottom	15.5	17.5 17.5	17.5	8.1 8.1	8.1	27.2 27.2	27.2	91.9 92.1	92.0	7.5 7.5	7.5	16.5 16.8	16.7		16.0 16.6	16.3	
18-Dec-15	Cloudy	Moderate	06:17	16.5	Surface	1.0	16.6 16.5	16.5	8.1 8.1	8.1	28.1 28.2	28.1	96.6 97.1	96.9	8.0 8.0	8.0	6.6 6.7	6.7	7.1	5.0 4.7	4.9	4.9
					Middle	8.3	16.3 16.3	16.3	8.1 8.1	8.1	28.0 28.2	28.1	94.5 95.8	95.2	7.8 7.9	7.9	7.3 7.0	7.2		5.2 5.1	5.2	
					Bottom	15.5	16.3 16.3	16.3	8.1 8.1	8.1	28.0 28.2	28.1	94.9 94.4	94.7	7.8 7.8	7.8	7.3 7.4	7.4		4.5 4.7	4.6	
21-Dec-15	Sunny	Moderate	14:32	15.6	Surface	1.0	16.3 16.3	16.3	8.2 8.2	8.2	31.7 32.3	32.0	95.7 96.2	96.0	7.8 7.7	7.7	3.5 3.5	3.5	3.6	3.6 3.7	3.7	3.5
					Middle	7.8	16.0 16.0	16.0	8.2 8.2	8.2	32.8 32.1	32.4	94.1 94.8	94.5	7.6 7.7	7.6	3.6 3.6	3.6		3.9 2.7	3.3	
					Bottom	14.6	16.0 16.1	16.0	8.2 8.2	8.2	33.7 32.3	33.0	93.2 94.1	93.7	7.5 7.6	7.6	3.6 3.6	3.6		3.4 3.8	3.6	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	16:34	15.4	Surface	1.0	16.6 16.6	16.6	8.1 8.1	8.1	25.8 26.3	26.1	94.9 95.5	95.2	7.9 7.9	7.9	7.9	4.6 4.7	4.7	5.0	2.8 3.4	3.1	4.1
					Middle	7.7	16.4 16.3	16.3	8.1 8.1	8.1	27.3 27.0	27.2	94.7 94.4	94.6	7.9 7.9	7.9		5.1 4.9	5.0		4.1 2.7	3.4	
					Bottom	14.4	16.3 16.4	16.4	8.1 8.1	8.1	29.3 28.4	28.9	94.8 95.0	94.9	7.8 7.8	7.8		5.4 5.2	5.3		6.7 5.0	5.9	
25-Dec-15	Cloudy	Moderate	08:12	18.5	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	25.5 25.9	25.7	95.7 96.2	96.0	8.0 8.0	8.0	8.0	7.7 7.8	7.8	7.9	10.8 10.3	10.6	10.8
					Middle	9.3	16.8 16.7	16.8	8.0 8.1	8.1	26.6 25.7	26.2	96.1 94.7	95.4	8.0 7.9	7.9		7.9 7.8	7.9		11.7 10.3	11.0	
					Bottom	17.5	16.7 16.8	16.7	8.1 8.0	8.0	25.8 26.4	26.1	93.3 95.9	94.6	7.8 7.9	7.9		7.9 7.9	7.9		10.9 10.6	10.8	
28-Dec-15	Sunny	Moderate	10:31	16.0	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	25.5 25.5	25.5	94.7 94.5	94.6	8.0 8.0	8.0	8.0	18.8 18.7	18.8	19.0	19.9 20.3	20.1	20.4
					Middle	8.0	16.0 16.0	16.0	8.1 8.1	8.1	25.5 25.5	25.5	94.5 94.4	94.5	8.0 8.0	8.0		18.9 19.1	19.0		20.4 22.0	21.2	
					Bottom	15.0	16.0 16.0	16.0	8.1 8.1	8.1	25.6 25.5	25.5	92.7 93.8	93.3	7.8 7.9	7.9		19.4 19.2	19.3		21.0 19.0	20.0	
30-Dec-15	Cloudy	Moderate	11:46	16.8	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	27.9 28.1	28.0	93.4 93.7	93.6	7.8 7.8	7.8	7.8	7.5 7.3	7.4	7.7	7.5 8.9	8.2	7.9
					Middle	8.4	16.0 16.0	16.0	8.1 8.1	8.1	28.0 27.9	28.0	94.9 92.9	93.9	7.9 7.8	7.8		7.7 7.8	7.8		7.7 7.9	7.8	
					Bottom	15.8	16.0 16.0	16.0	8.1 8.1	8.1	28.1 28.0	28.1	96.0 95.4	95.7	8.0 8.0	8.0		7.8 7.8	7.8		8.2 7.0	7.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	18:06	12.1	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	27.4 27.2	27.3	85.4 88.6	87.0	6.2 6.4	6.3	6.2	3.4 3.5	3.5	3.5	3.1 2.7	2.9	2.9
					Middle	6.1	23.9 23.9	23.9	8.0 8.1	8.0	30.0 29.9	30.0	85.6 84.7	85.2	6.1 6.0	6.1		3.4 3.4	3.4		2.6 2.4	2.5	
					Bottom	11.1	23.9 23.9	23.9	8.0 8.0	8.0	30.2 30.3	30.2	85.0 89.1	87.1	6.0 6.3	6.2		3.5 3.4	3.5		2.8 3.6	3.2	
4-Dec-15	Cloudy	Moderate	06:08	12.5	Surface	1.0	22.7 22.7	22.7	8.2 8.2	8.2	25.6 25.6	25.6	86.0 85.0	85.5	6.4 6.3	6.4	6.2	2.9 2.8	2.9	3.0	3.6 2.4	3.0	3.2
					Middle	6.3	24.0 24.0	24.0	8.1 8.1	8.1	30.0 30.1	30.1	86.9 83.6	85.3	6.2 5.9	6.0		2.7 3.0	2.9		2.8 2.8	2.8	
					Bottom	11.5	23.9 24.0	24.0	8.1 8.1	8.1	30.3 30.3	30.3	84.4 86.4	85.4	6.0 6.1	6.1		3.1 3.2	3.2		3.7 3.7	3.7	
7-Dec-15	Cloudy	Moderate	09:58	12.3	Surface	1.0	22.7 22.6	22.7	8.2 8.2	8.2	30.7 30.6	30.6	87.9 89.8	88.9	6.4 6.5	6.4	6.4	2.7 2.7	2.7	2.7	4.7 4.1	4.4	4.1
					Middle	6.2	22.8 22.9	22.9	8.2 8.2	8.2	30.9 31.1	31.0	88.2 87.2	87.7	6.4 6.3	6.3		2.7 2.7	2.7		3.6 4.6	4.1	
					Bottom	11.3	22.9 22.8	22.8	8.2 8.2	8.2	31.0 31.0	31.0	87.5 86.5	87.0	6.3 6.2	6.3		2.7 2.7	2.7		3.6 4.2	3.9	
9-Dec-15	Rainy	Moderate	11:31	12.7	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	31.0 31.0	31.0	84.4 88.9	86.7	6.1 6.5	6.3	6.2	3.3 3.2	3.3	3.6	3.6 3.6	3.6	4.3
					Middle	6.4	22.4 22.4	22.4	8.2 8.2	8.2	31.2 31.2	31.2	83.9 84.5	84.2	6.1 6.1	6.1		3.7 3.8	3.8		4.2 4.1	4.2	
					Bottom	11.7	22.4 22.4	22.4	8.2 8.2	8.2	31.2 31.2	31.2	84.0 84.9	84.5	6.1 6.2	6.1		3.8 3.7	3.8		5.1 5.1	5.1	
11-Dec-15	Sunny	Moderate	13:10	13.3	Surface	1.0	22.0 21.9	22.0	8.2 8.2	8.2	31.1 31.1	31.1	85.3 85.5	85.4	6.2 6.3	6.2	6.2	4.5 4.7	4.6	4.7	2.8 3.3	3.1	3.8
					Middle	6.7	22.1 22.1	22.1	8.2 8.2	8.2	31.4 31.4	31.4	85.1 86.5	85.8	6.2 6.3	6.2		4.8 4.6	4.7		3.0 3.5	3.3	
					Bottom	12.3	22.1 22.1	22.1	8.2 8.2	8.2	31.4 31.4	31.4	85.4 87.7	86.6	6.2 6.4	6.3		4.9 4.7	4.8		4.5 5.3	4.9	
14-Dec-15	Rainy	Moderate	15:17	12.5	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	28.8 28.8	28.8	88.6 90.6	89.6	6.6 6.7	6.7	6.6	4.5 4.4	4.5	5.7	4.8 5.0	4.9	5.4
					Middle	6.3	21.9 21.8	21.9	8.2 8.1	8.2	30.4 30.3	30.3	89.2 88.4	88.8	6.6 6.5	6.5		6.2 6.2	6.2		5.8 6.1	6.0	
					Bottom	11.5	21.9 21.8	21.9	8.1 8.1	8.1	30.5 30.6	30.6	87.3 87.3	87.3	6.4 6.4	6.4		6.5 6.5	6.5		5.4 5.0	5.2	
16-Dec-15	Sunny	Moderate	16:55	13.3	Surface	1.0	21.1 21.0	21.1	8.2 8.2	8.2	27.9 27.8	27.9	84.8 91.6	88.2	6.4 6.9	6.7	6.7	4.4 4.5	4.5	4.5	3.7 5.4	4.6	8.3
					Middle	6.7	21.4 21.4	21.4	8.2 8.1	8.2	29.7 29.6	29.6	85.2 91.4	88.3	6.3 6.8	6.6		4.4 4.6	4.5		8.1 10.2	9.2	
					Bottom	12.3	21.4 21.3	21.4	8.1 8.2	8.1	29.5 29.7	29.6	85.1 86.8	86.0	6.3 6.5	6.4		4.4 4.3	4.4		10.3 11.9	11.1	
18-Dec-15	Sunny	Moderate	13:00	12.4	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.6 30.6	30.6	89.4 89.5	89.5	6.7 6.8	6.7	6.7	5.5 5.6	5.6	5.7	5.1 4.8	5.0	5.2
					Middle	6.2	20.4 20.4	20.4	8.2 8.2	8.2	30.9 30.9	30.9	86.9 89.0	88.0	6.5 6.7	6.6		5.8 5.6	5.7		4.7 5.2	5.0	
					Bottom	11.4	20.4 20.4	20.4	8.2 8.2	8.2	30.9 30.9	30.9	86.6 88.9	87.8	6.5 6.7	6.6		5.8 5.8	5.8		5.1 5.8	5.5	
21-Dec-15	Cloudy	Moderate	15:53	13.6	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	30.5 30.5	30.5	85.5 87.3	86.4	6.5 6.6	6.5	6.6	2.9 2.7	2.8	3.0	6.5 5.8	6.2	5.2
					Middle	6.8	20.2 20.2	20.2	8.2 8.2	8.2	30.7 30.7	30.7	89.4 85.2	87.3	6.8 6.4	6.6		3.1 3.2	3.2		5.0 4.1	4.6	
					Bottom	12.6	20.2 20.2	20.2	8.2 8.2	8.2	30.7 30.7	30.7	86.6 91.0	88.8	6.6 6.9	6.7		3.0 3.2	3.1		5.4 4.1	4.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	10:41	12.3	Surface	1.0	20.1 20.1	20.1	8.1 8.1	8.1	29.5 29.5	29.5	87.6 87.6	87.6	6.7 6.7	6.7	6.7	3.5 3.3	3.4	3.4	3.3 2.7	3.0	3.9
					Middle	6.2	20.1 20.1	20.1	8.1 8.1	8.1	30.0 29.8	29.9	86.8 86.3	86.6	6.6 6.6	6.6		3.4 3.3	3.4		5.1 3.9	4.5	
					Bottom	11.3	20.1 20.1	20.1	8.1 8.1	8.1	29.9 30.0	30.0	87.9 87.4	87.7	6.7 6.7	6.7		3.3 3.2	3.3		4.6 3.6	4.1	
25-Dec-15	Cloudy	Moderate	13:07	12.6	Surface	1.0	20.3 20.1	20.2	8.2 8.2	8.2	27.6 27.5	27.6	87.8 88.9	88.4	6.8 6.9	6.8	6.7	5.2 5.4	5.3	5.4	5.5 6.3	5.9	5.9
					Middle	6.3	20.3 20.3	20.3	8.1 8.2	8.2	29.5 29.4	29.5	87.0 86.3	86.7	6.6 6.6	6.6		5.4 5.3	5.4		6.1 6.2	6.2	
					Bottom	11.6	20.3 20.3	20.3	8.1 8.1	8.1	29.6 29.6	29.6	88.0 87.1	87.6	6.7 6.6	6.6		5.3 5.4	5.4		6.1 5.0	5.6	
28-Dec-15	Sunny	Moderate	14:55	12.0	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	28.4 28.7	28.5	88.6 89.4	89.0	6.9 6.9	6.9	6.9	5.1 5.5	5.3	5.3	5.3 5.7	5.5	5.9
					Middle	6.0	19.8 19.8	19.8	8.2 8.2	8.2	29.4 29.4	29.4	90.3 87.9	89.1	6.9 6.8	6.8		5.3 5.4	5.4		6.2 6.4	6.3	
					Bottom	11.0	19.8 19.8	19.8	8.2 8.2	8.2	29.5 29.3	29.4	88.8 87.0	87.9	6.8 6.7	6.8		5.4 5.2	5.3		6.0 5.8	5.9	
30-Dec-15	Cloudy	Moderate	16:17	13.4	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.2 29.2	29.2	89.3 87.1	88.2	6.9 6.7	6.8	6.8	3.8 3.7	3.8	4.1	4.5 2.8	3.7	3.8
					Middle	6.7	19.7 19.7	19.7	8.2 8.2	8.2	29.7 29.8	29.8	89.6 87.7	88.7	6.9 6.7	6.8		4.4 4.1	4.3		5.1 3.2	4.2	
					Bottom	12.4	19.7 19.7	19.7	8.2 8.2	8.2	29.9 29.8	29.8	87.8 86.5	87.2	6.7 6.6	6.7		4.2 4.0	4.1		3.2 3.7	3.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	11:58	12.3	Surface	1.0	23.7 23.8	23.8	8.1 8.1	8.1	25.8 25.8	25.8	85.5 85.2	85.4	6.2 6.2	6.2	6.2	5.3 5.6	5.5	5.6	2.7 3.8	3.3	3.3
					Middle	6.2	23.8 23.8	23.8	8.1 8.1	8.1	27.4 27.3	27.4	85.0 83.7	84.4	6.1 6.1	6.1		5.5 5.6	5.6		3.6 3.5	3.6	
					Bottom	11.3	23.9 23.8	23.9	8.0 8.0	8.0	27.9 27.9	27.9	84.6 83.6	84.1	6.1 6.0	6.1		5.6 5.6	5.6		3.2 2.9	3.1	
4-Dec-15	Cloudy	Moderate	14:25	12.5	Surface	1.0	23.7 23.6	23.7	8.1 8.2	8.2	29.0 28.7	28.9	83.8 82.9	83.4	6.0 6.0	6.0	6.0	5.0 5.2	5.1	5.4	2.3 2.4	2.4	2.7
					Middle	6.3	24.0 23.9	24.0	8.1 8.1	8.1	31.1 31.1	31.1	82.0 83.3	83.7	5.9 5.9	5.9		5.5 5.5	5.5		2.3 3.0	2.7	
					Bottom	11.5	23.9 24.0	23.9	8.1 8.1	8.1	31.2 31.3	31.2	83.9 85.9	84.9	5.9 6.1	6.0		5.4 5.6	5.5		3.7 2.2	3.0	
7-Dec-15	Cloudy	Moderate	16:32	12.5	Surface	1.0	22.6 22.6	22.6	8.2 8.2	8.2	30.8 30.9	30.8	86.4 91.4	88.9	6.2 6.6	6.4	6.4	3.3 3.1	3.2	3.4	4.2 5.3	4.8	5.4
					Middle	6.3	22.8 22.8	22.8	8.2 8.2	8.2	31.7 31.7	31.7	89.6 86.2	87.9	6.4 6.2	6.3		3.4 3.5	3.5		4.8 4.5	4.7	
					Bottom	11.5	22.9 22.9	22.9	8.2 8.2	8.2	31.8 31.8	31.8	89.0 85.5	87.3	6.4 6.1	6.3		3.5 3.5	3.5		6.7 6.4	6.6	
9-Dec-15	Rainy	Moderate	17:21	12.7	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	31.1 31.1	31.1	86.9 88.4	87.7	6.3 6.4	6.4	6.4	5.8 5.4	5.6	6.4	7.6 7.0	7.3	8.2
					Middle	6.4	22.3 22.3	22.3	8.2 8.2	8.2	31.1 31.1	31.1	88.1 88.0	88.1	6.4 6.4	6.4		6.6 6.7	6.7		7.6 7.8	7.7	
					Bottom	11.7	22.3 22.3	22.3	8.2 8.2	8.2	31.1 31.1	31.1	84.9 90.1	87.5	6.2 6.5	6.4		6.9 6.7	6.8		9.3 9.6	9.5	
11-Dec-15	Sunny	Moderate	06:59	13.4	Surface	1.0	22.1 22.1	22.1	8.2 8.1	8.2	30.9 30.8	30.9	87.7 89.3	88.5	6.4 6.5	6.5	6.5	10.4 11.1	10.8	11.5	10.0 10.8	10.4	9.9
					Middle	6.7	22.1 22.1	22.1	8.1 8.2	8.2	30.8 30.9	30.9	90.5 84.0	87.3	6.6 6.1	6.4		11.5 11.3	11.4		9.0 10.0	9.5	
					Bottom	12.4	22.1 22.1	22.1	8.2 8.1	8.2	30.9 30.8	30.8	85.0 89.3	87.2	6.2 6.5	6.4		12.6 12.2	12.4		9.9 9.7	9.8	
14-Dec-15	Rainy	Moderate	09:16	12.1	Surface	1.0	21.6 21.6	21.6	8.1 8.1	8.1	28.6 28.6	28.6	86.4 86.8	86.6	6.4 6.4	6.4	6.6	10.0 10.2	10.1	10.3	7.7 7.9	7.8	8.3
					Middle	6.1	21.7 21.7	21.7	8.1 8.1	8.1	29.4 29.3	29.4	90.8 90.5	90.7	6.8 6.7	6.7		10.6 10.4	10.5		8.0 8.5	8.3	
					Bottom	11.1	21.7 21.7	21.7	8.1 8.1	8.1	29.6 29.7	29.6	88.5 88.9	88.7	6.6 6.6	6.6		10.2 10.5	10.4		8.1 9.3	8.7	
16-Dec-15	Sunny	Moderate	10:50	13.3	Surface	1.0	21.0 20.9	21.0	8.2 8.2	8.2	28.3 28.3	28.3	87.5 90.2	88.9	6.6 6.8	6.7	6.7	4.2 4.0	4.1	4.3	4.6 5.8	5.2	8.1
					Middle	6.7	21.4 21.4	21.4	8.1 8.1	8.1	29.1 29.3	29.2	89.9 86.6	88.3	6.7 6.5	6.6		4.5 4.3	4.4		7.1 7.2	7.2	
					Bottom	12.3	21.5 21.3	21.4	8.1 8.1	8.1	29.5 29.1	29.3	87.8 89.1	88.5	6.5 6.7	6.6		4.2 4.7	4.5		11.6 12.4	12.0	
18-Dec-15	Cloudy	Moderate	05:06	12.6	Surface	1.0	19.7 19.8	19.7	8.2 8.2	8.2	29.3 29.3	29.3	87.1 88.5	87.8	6.7 6.7	6.7	6.7	6.5 6.7	6.6	7.7	3.0 3.0	3.0	3.3
					Middle	6.3	20.2 20.2	20.2	8.2 8.2	8.2	30.0 30.0	30.0	87.2 87.0	87.1	6.6 6.7	6.7		8.3 8.1	8.2		3.4 3.9	3.7	
					Bottom	11.6	20.3 20.1	20.2	8.2 8.2	8.2	30.2 30.0	30.1	86.7 86.9	86.8	6.6 6.6	6.6		8.0 8.5	8.3		3.0 3.2	3.1	
21-Dec-15	Sunny	Moderate	08:36	13.4	Surface	1.0	20.0 20.0	20.0	8.2 8.1	8.2	30.8 30.7	30.8	86.9 92.3	89.6	6.6 7.0	6.8	6.7	2.8 2.7	2.8	2.8	3.8 4.8	4.3	5.5
					Middle	6.7	20.2 20.2	20.2	8.1 8.1	8.1	31.0 31.0	31.0	89.2 85.1	87.2	6.7 6.4	6.6		2.9 2.9	2.9		2.5 3.8	3.2	
					Bottom	12.4	20.2 20.2	20.2	8.1 8.1	8.1	31.0 30.9	31.0	86.0 91.5	88.8	6.5 6.9	6.7		2.8 2.8	2.8		8.0 9.7	8.9	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	17:00	12.5	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	28.4 28.3	28.4	88.2 87.1	87.7	6.8 6.7	6.7	6.7	11.1 11.2	11.2	11.2	8.3 10.2	9.3	5.8
					Middle	6.3	20.1 20.1	20.1	8.2 8.2	8.2	31.0 31.0	31.0	89.4 87.7	88.6	6.8 6.6	6.7		11.2 11.1	11.2		3.6 4.1	3.9	
					Bottom	11.5	20.2 20.1	20.1	8.2 8.2	8.2	31.1 31.0	31.1	87.0 86.9	87.0	6.6 6.6	6.6		11.2 11.3	11.3		4.4 3.8	4.1	
25-Dec-15	Cloudy	Moderate	07:26	12.2	Surface	1.0	20.2 20.1	20.2	8.1 8.1	8.1	26.8 26.7	26.7	86.6 87.9	87.3	6.7 6.8	6.8	6.8	9.1 9.3	9.2	9.5	7.7 7.8	7.8	8.4
					Middle	6.1	20.3 20.3	20.3	8.1 8.1	8.1	28.5 28.5	28.5	85.9 90.0	88.0	6.6 6.9	6.7		9.7 9.6	9.7		9.2 9.2	9.2	
					Bottom	11.2	20.3 20.3	20.3	8.1 8.1	8.1	28.5 28.5	28.5	85.9 85.6	85.8	6.6 6.5	6.6		9.7 9.7	9.7		7.8 8.6	8.2	
28-Dec-15	Sunny	Moderate	09:01	12.4	Surface	1.0	19.5 19.5	19.5	8.1 8.1	8.1	27.9 27.8	27.9	87.5 88.7	88.1	6.8 6.9	6.9	6.9	7.7 7.4	7.6	7.8	8.5 8.8	8.7	9.6
					Middle	6.2	19.7 19.6	19.6	8.1 8.1	8.1	28.2 27.9	28.0	87.3 87.9	87.6	6.8 6.8	6.8		7.8 7.7	7.8		10.0 10.4	10.2	
					Bottom	11.4	19.8 19.7	19.8	8.1 8.1	8.1	28.6 28.6	28.6	86.7 86.8	86.8	6.7 6.7	6.7		7.8 7.9	7.9		9.2 10.4	9.8	
30-Dec-15	Cloudy	Moderate	10:27	13.4	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	28.5 28.5	28.5	87.4 87.5	87.5	6.8 6.8	6.8	6.8	4.6 4.7	4.7	6.0	3.9 3.8	3.9	3.9
					Middle	6.7	19.7 19.7	19.7	8.1 8.1	8.1	29.2 29.2	29.2	87.5 85.8	86.7	6.7 6.6	6.7		7.2 7.1	7.2		3.7 4.3	4.0	
					Bottom	12.4	19.7 19.7	19.7	8.1 8.1	8.1	29.2 29.2	29.2	88.2 86.3	87.3	6.8 6.7	6.7		6.0 6.2	6.1		3.5 4.0	3.8	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	18:29	10.0	Surface	1.0	20.8 20.8	20.8	8.2 8.2	8.2	27.9 24.6	26.3	98.9 99.2	99.1	7.4 7.5	7.5	7.5	2.5 2.6	2.6	2.8	3.7 4.9	4.3	5.0
					Middle	5.0	20.7 20.7	20.7	8.2 8.2	8.2	26.7 30.7	28.7	97.3 96.5	96.9	7.4 7.4	7.4		2.7 2.6	2.7		5.5 5.0	5.3	
					Bottom	9.0	20.7 20.7	20.7	8.2 8.2	8.2	31.2 27.5	29.3	95.6 95.7	95.7	7.3 7.4	7.4		2.9 3.0	3.0		5.5 5.3	5.4	
4-Dec-15	Cloudy	Moderate	05:03	9.6	Surface	1.0	19.3 19.3	19.3	8.1 8.1	8.1	30.2 30.2	30.2	93.6 94.7	94.2	7.1 7.0	7.1	7.1	1.7 1.7	1.7	1.8	2.8 3.4	3.1	2.8
					Middle	4.8	20.0 20.2	20.1	8.1 8.1	8.1	31.5 31.0	31.2	93.0 91.3	92.2	7.0 7.0	7.0		1.8 1.7	1.8		2.3 2.9	2.6	
					Bottom	8.6	20.3 20.3	20.3	8.1 8.1	8.1	34.0 33.4	33.7	91.9 90.9	91.4	6.9 6.9	6.9		1.8 1.8	1.8		2.8 2.5	2.7	
7-Dec-15	Cloudy	Moderate	08:51	10.0	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	36.1 36.0	36.0	93.3 93.1	93.2	6.9 6.9	6.9	6.9	2.3 2.3	2.3	2.5	4.2 3.8	4.0	4.0
					Middle	5.0	19.5 19.5	19.5	8.2 8.2	8.2	36.1 36.1	36.1	92.0 92.4	92.2	6.8 6.9	6.8		2.5 2.4	2.5		4.2 3.5	3.9	
					Bottom	9.0	19.5 19.5	19.5	8.2 8.2	8.2	36.1 36.1	36.1	91.5 91.6	91.6	6.9 6.8	6.8		2.8 2.7	2.8		3.0 5.1	4.1	
9-Dec-15	Rainy	Moderate	10:29	10.1	Surface	1.0	19.1 19.1	19.1	8.2 8.2	8.2	36.2 36.2	36.2	91.6 91.4	91.5	6.8 6.8	6.8	6.8	3.0 3.0	3.0	3.1	3.2 3.3	3.3	3.1
					Middle	5.1	19.1 19.1	19.1	8.2 8.2	8.2	36.3 36.3	36.3	91.3 91.5	91.4	6.8 6.8	6.8		3.0 3.1	3.1		2.6 2.7	2.7	
					Bottom	9.1	19.1 19.1	19.1	8.2 8.2	8.2	36.3 36.3	36.3	91.3 91.5	91.4	6.8 6.8	6.8		3.0 3.2	3.1		2.9 3.4	3.2	
11-Dec-15	Sunny	Moderate	13:38	10.3	Surface	1.0	18.9 18.9	18.9	8.2 8.2	8.2	30.4 29.7	30.1	96.8 90.9	93.9	7.4 7.1	7.3	7.2	4.1 4.3	4.2	4.6	3.9 4.8	4.4	4.2
					Middle	5.2	18.8 18.8	18.8	8.2 8.2	8.2	29.9 31.0	30.4	89.9 91.3	90.6	7.0 7.1	7.0		4.7 4.8	4.8		3.6 3.1	3.4	
					Bottom	9.3	18.8 18.8	18.8	8.2 8.2	8.2	30.0 32.5	31.2	89.7 91.2	90.5	7.0 7.1	7.0		4.6 4.8	4.7		4.5 5.3	4.9	
14-Dec-15	Rainy	Moderate	15:48	10.1	Surface	1.0	18.5 18.5	18.5	8.2 8.1	8.2	26.8 27.7	27.3	91.9 91.4	91.7	7.3 7.3	7.3	7.3	4.4 4.2	4.3	4.6	6.3 6.0	6.2	5.8
					Middle	5.1	18.5 18.5	18.5	8.1 8.1	8.1	28.0 29.3	28.7	91.3 90.5	90.9	7.2 7.2	7.2		4.7 4.7	4.7		4.5 6.4	5.5	
					Bottom	9.1	18.5 18.5	18.5	8.1 8.1	8.1	30.6 28.2	29.4	89.9 90.1	90.0	7.1 7.2	7.2		4.8 4.8	4.8		5.6 5.9	5.8	
16-Dec-15	Sunny	Moderate	17:21	10.1	Surface	1.0	18.1 18.1	18.1	8.2 8.2	8.2	31.7 32.5	32.1	93.1 97.8	95.5	7.3 7.5	7.4	7.3	2.8 2.8	2.8	2.9	6.8 7.5	7.2	8.0
					Middle	5.1	18.1 18.1	18.1	8.2 8.2	8.2	32.1 33.2	32.6	91.3 94.1	92.7	7.1 7.3	7.2		2.8 2.9	2.9		8.6 7.6	8.1	
					Bottom	9.1	18.1 18.1	18.1	8.2 8.2	8.2	34.1 32.2	33.2	92.0 90.2	91.1	7.2 7.1	7.1		2.9 2.8	2.9		8.8 8.4	8.6	
18-Dec-15	Sunny	Moderate	13:44	10.7	Surface	1.0	17.4 17.4	17.4	8.1 8.1	8.1	29.7 31.0	30.3	96.4 99.2	97.8	7.7 7.9	7.8	7.9	4.4 4.2	4.3	4.6	5.5 6.1	5.8	5.3
					Middle	5.4	17.3 17.3	17.3	8.1 8.1	8.1	29.9 32.0	31.0	96.8 103.2	100.0	7.8 8.2	8.0		4.8 4.5	4.7		5.4 4.9	5.2	
					Bottom	9.7	17.3 17.3	17.3	8.1 8.1	8.1	32.5 30.1	31.3	106.6 97.7	102.2	8.4 7.8	8.1		5.0 4.6	4.8		5.2 4.8	5.0	
21-Dec-15	Cloudy	Moderate	08:10	10.3	Surface	1.0	16.8 16.9	16.9	8.1 8.1	8.1	36.2 36.1	36.1	91.4 90.9	91.2	7.1 7.1	7.1	7.1	2.4 2.4	2.4	2.5	5.8 4.3	5.1	4.5
					Middle	5.2	16.9 16.9	16.9	8.1 8.1	8.1	36.1 36.2	36.2	91.1 91.0	91.1	7.1 7.1	7.1		2.5 2.5	2.5		4.4 5.9	5.2	
					Bottom	9.3	16.9 16.9	16.9	8.1 8.1	8.1	36.2 36.1	36.1	91.1 91.1	91.1	7.1 7.1	7.1		2.4 2.5	2.5		4.1 2.4	3.3	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	09:52	10.6	Surface	1.0	16.8 16.8	16.8	8.1 8.1	8.1	35.3 35.5	35.4	90.8 90.6	90.7	7.1 7.1	7.1	7.1	3.7 3.7	3.7	3.9	3.3 4.2	3.8	3.3
					Middle	5.3	16.8 16.8	16.8	8.1 8.1	8.1	35.7 35.8	35.8	90.2 90.5	90.4	7.1 7.1	7.1		3.9 3.7	3.8		3.3 2.2	2.8	
					Bottom	9.6	16.8 16.8	16.8	8.1 8.1	8.1	35.9 35.9	35.9	88.4 87.8	88.1	6.9 6.9	6.9		4.3 4.1	4.2		3.0 3.4	3.2	
25-Dec-15	Cloudy	Moderate	13:12	10.4	Surface	1.0	16.8 16.8	16.8	8.1 8.1	8.1	27.6 29.3	28.4	98.3 104.7	101.5	7.9 8.3	8.1	8.1	5.3 5.4	5.4	5.4	5.1 5.9	5.5	5.5
					Middle	5.2	16.9 16.9	16.9	8.1 8.1	8.1	29.5 32.4	30.9	97.2 100.4	98.8	7.9 8.0	8.0		5.4 5.4	5.4		5.1 5.6	5.4	
					Bottom	9.4	16.8 16.8	16.8	8.1 8.1	8.1	30.4 33.0	31.7	96.4 97.0	96.7	7.9 7.9	7.9		5.4 5.6	5.5		5.8 5.4	5.6	
28-Dec-15	Sunny	Moderate	15:30	10.4	Surface	1.0	16.4 16.4	16.4	8.2 8.2	8.2	28.2 27.2	27.7	93.5 93.0	93.3	7.7 7.7	7.7	7.7	2.8 2.8	2.8	2.9	4.0 4.6	4.3	4.3
					Middle	5.2	16.4 16.4	16.4	8.1 8.2	8.2	27.7 27.2	27.4	93.4 92.7	93.1	7.7 7.7	7.7		2.9 2.9	2.9		3.3 3.9	3.6	
					Bottom	9.4	16.4 16.4	16.4	8.1 8.2	8.2	29.7 28.3	29.0	93.4 93.2	93.3	7.7 7.7	7.7		3.1 3.1	3.1		5.6 4.2	4.9	
30-Dec-15	Cloudy	Moderate	17:12	10.2	Surface	1.0	16.3 16.3	16.3	8.2 8.2	8.2	28.7 29.5	29.1	94.4 96.5	95.5	7.8 7.9	7.9	7.9	2.4 2.4	2.4	2.4	3.5 3.9	3.7	3.6
					Middle	5.1	16.3 16.3	16.3	8.2 8.2	8.2	29.9 28.9	29.4	97.1 94.3	95.7	7.9 7.8	7.9		2.5 2.4	2.5		3.5 3.0	3.3	
					Bottom	9.2	16.3 16.3	16.3	8.2 8.2	8.2	29.0 30.8	29.9	94.6 99.3	97.0	7.8 8.1	7.9		2.4 2.4	2.4		4.6 2.8	3.7	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	11:55	10.0	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	29.4 29.3	29.3	93.0 93.5	93.3	7.1 7.1	7.1	7.1	2.6 2.5	2.6	3.0	3.6 3.2	3.4	3.6
					Middle	5.0	20.4 20.4	20.4	8.1 8.1	8.1	29.9 29.6	29.7	93.0 93.3	93.2	7.0 7.0	7.0		3.2 2.8	3.0		2.5 3.7	3.1	
					Bottom	9.0	20.4 20.4	20.4	8.0 8.0	8.0	30.1 30.5	30.3	92.4 91.9	92.2	7.0 7.0	7.0		3.2 3.3	3.3		3.8 4.8	4.3	
4-Dec-15	Cloudy	Moderate	15:55	9.7	Surface	1.0	19.6 19.7	19.7	8.2 8.2	8.2	26.5 29.0	27.8	94.8 95.5	95.2	7.4 7.4	7.4	7.4	2.0 2.0	2.0	2.1	4.2 3.8	4.0	4.2
					Middle	4.9	19.8 19.8	19.8	8.2 8.2	8.2	27.1 30.5	28.8	93.6 95.1	94.4	7.3 7.3	7.3		2.1 2.1	2.1		3.9 4.4	4.2	
					Bottom	8.7	19.9 20.2	20.0	8.3 8.2	8.2	34.1 29.5	31.8	94.7 93.0	93.9	7.2 7.2	7.2		2.2 2.3	2.3		4.2 4.5	4.4	
7-Dec-15	Cloudy	Moderate	17:31	10.0	Surface	1.0	19.6 19.6	19.6	8.3 8.3	8.3	30.8 31.8	31.3	95.6 94.5	95.1	7.2 7.2	7.2	7.2	2.2 2.2	2.2	2.3	2.7 3.8	3.3	4.6
					Middle	5.0	19.6 19.6	19.6	8.3 8.3	8.3	32.1 31.0	31.6	93.9 93.6	93.8	7.1 7.1	7.1		2.3 2.3	2.3		4.9 4.8	4.9	
					Bottom	9.0	19.6 19.6	19.6	8.3 8.3	8.3	32.7 31.2	32.0	92.6 92.6	92.6	7.1 7.1	7.1		2.4 2.3	2.4		6.4 5.0	5.7	
9-Dec-15	Rainy	Moderate	17:51	10.1	Surface	1.0	19.0 19.1	19.1	8.2 8.2	8.2	30.0 30.2	30.1	104.8 92.1	98.5	8.1 7.1	7.6	7.5	5.4 5.3	5.4	5.6	6.0 5.1	5.6	5.2
					Middle	5.1	19.0 19.1	19.0	8.2 8.2	8.2	31.0 30.2	30.6	100.8 91.4	96.1	7.8 7.1	7.4		5.7 5.4	5.6		4.9 5.0	5.0	
					Bottom	9.1	19.1 19.0	19.0	8.2 8.2	8.2	30.2 31.0	30.6	90.0 92.4	91.2	7.0 7.2	7.1		5.7 5.8	5.8		4.4 5.4	4.9	
11-Dec-15	Sunny	Moderate	06:41	10.1	Surface	1.0	18.8 18.8	18.8	8.1 8.1	8.1	36.2 36.3	36.2	89.8 90.0	89.9	6.8 6.8	6.8	6.8	7.2 7.4	7.3	7.3	8.7 8.8	8.8	9.8
					Middle	5.1	18.8 18.8	18.8	8.1 8.1	8.1	36.3 36.2	36.2	89.6 88.9	89.3	6.7 6.7	6.7		7.4 7.2	7.3		9.7 8.9	9.3	
					Bottom	9.1	18.8 18.8	18.8	8.1 8.1	8.1	36.2 36.3	36.2	88.5 89.5	89.0	6.6 6.7	6.7		7.4 7.4	7.4		10.6 11.8	11.2	
14-Dec-15	Rainy	Moderate	08:54	10.2	Surface	1.0	18.3 18.3	18.3	8.1 8.1	8.1	32.1 32.3	32.2	93.7 93.7	93.7	7.3 7.3	7.3	7.3	4.5 4.5	4.5	4.8	5.6 5.6	5.6	6.9
					Middle	5.1	18.3 18.3	18.3	8.1 8.1	8.1	33.4 32.7	33.1	94.1 93.9	94.0	7.2 7.2	7.2		4.8 4.7	4.8		7.3 6.7	7.0	
					Bottom	9.2	18.4 18.3	18.3	8.1 8.1	8.1	33.9 33.4	33.7	92.0 92.4	92.2	7.1 7.2	7.1		5.0 4.9	5.0		8.2 7.7	8.0	
16-Dec-15	Sunny	Moderate	10:25	10.6	Surface	1.0	17.7 17.7	17.7	8.0 8.1	8.1	33.5 33.5	33.5	91.2 91.5	91.4	7.1 7.1	7.1	7.1	4.2 4.3	4.3	4.3	6.0 5.6	5.8	6.1
					Middle	5.3	17.7 17.7	17.7	8.1 8.0	8.0	33.5 33.5	33.5	91.0 91.1	91.1	7.1 7.1	7.1		4.3 4.3	4.3		4.7 6.4	5.6	
					Bottom	9.6	17.7 17.7	17.7	8.0 8.0	8.0	33.5 33.5	33.5	90.7 91.0	90.9	7.1 7.1	7.1		4.2 4.3	4.3		6.3 7.6	7.0	
18-Dec-15	Cloudy	Moderate	04:34	10.3	Surface	1.0	16.9 16.8	16.9	8.1 8.1	8.1	35.4 35.3	35.3	93.0 95.1	94.1	7.3 7.5	7.4	7.4	5.0 5.2	5.1	5.1	5.8 5.9	5.9	5.7
					Middle	5.2	16.9 16.9	16.9	8.0 8.1	8.1	35.5 35.4	35.4	94.3 92.6	93.5	7.4 7.2	7.3		5.0 4.6	4.8		6.6 5.4	6.0	
					Bottom	9.3	16.9 16.9	16.9	8.0 8.1	8.1	35.5 35.5	35.5	94.0 92.9	93.5	7.3 7.3	7.3		5.6 5.3	5.5		5.4 5.2	5.3	
21-Dec-15	Sunny	Moderate	16:17	10.6	Surface	1.0	16.9 16.9	16.9	8.2 8.2	8.2	29.5 30.6	30.1	93.6 97.8	95.7	7.6 7.8	7.7	7.7	2.9 3.1	3.0	3.3	6.2 6.0	6.1	5.6
					Middle	5.3	16.9 16.9	16.9	8.2 8.2	8.2	31.8 29.7	30.7	96.3 93.1	94.7	7.7 7.6	7.6		3.5 3.4	3.5		4.3 5.9	5.1	
					Bottom	9.6	16.9 16.9	16.9	8.2 8.2	8.2	33.3 29.9	31.6	94.7 93.1	93.9	7.6 7.5	7.6		3.4 3.2	3.3		5.9 5.3	5.6	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	18:10	10.7	Surface	1.0	16.6 16.7	16.7	8.1 8.1	8.1	26.6 25.7	26.1	95.5 95.5	95.5	7.9 7.9	7.9	7.8	2.2 2.2	2.2	2.3	4.3 4.2	4.3	4.1
					Middle	5.4	16.7 16.7	16.7	8.1 8.1	8.1	26.9 28.8	27.8	92.5 93.3	92.9	7.7 7.6	7.7		2.2 2.3	2.3		3.2 4.6	3.9	
					Bottom	9.7	16.7 16.7	16.7	8.1 8.1	8.1	27.2 28.7	28.0	92.6 93.6	93.1	7.7 7.4	7.5		2.4 2.3	2.4		2.9 5.3	4.1	
25-Dec-15	Cloudy	Moderate	06:58	10.1	Surface	1.0	16.9 16.9	16.9	8.0 8.0	8.0	33.7 33.8	33.8	89.0 90.7	89.9	7.0 7.2	7.1	7.1	7.6 7.4	7.5	7.6	10.4 11.1	10.8	11.0
					Middle	5.1	16.9 16.9	16.9	8.0 8.0	8.0	33.7 33.8	33.8	88.8 89.0	88.9	7.0 7.0	7.0		7.6 7.5	7.6		10.9 11.3	11.1	
					Bottom	9.1	16.9 16.9	16.9	8.0 8.0	8.0	33.8 33.8	33.8	88.8 88.8	88.8	7.0 7.0	7.0		7.6 7.7	7.7		11.2 10.8	11.0	
28-Dec-15	Sunny	Moderate	08:57	10.6	Surface	1.0	16.1 16.1	16.1	8.0 8.0	8.0	32.0 32.0	32.0	93.9 94.2	94.1	7.7 7.6	7.6	7.6	4.8 4.7	4.8	5.0	7.0 7.1	7.1	6.8
					Middle	5.3	16.1 16.1	16.1	8.0 8.0	8.0	32.0 32.2	32.1	94.1 94.0	94.1	7.6 7.6	7.6		4.9 4.9	4.9		7.0 6.2	6.6	
					Bottom	9.6	16.1 16.1	16.1	8.0 8.0	8.0	32.2 32.1	32.1	93.9 93.8	93.9	7.6 7.6	7.6		5.2 5.3	5.3		7.3 6.2	6.8	
30-Dec-15	Cloudy	Moderate	10:12	10.2	Surface	1.0	16.1 16.1	16.1	8.1 8.1	8.1	33.1 33.1	33.1	94.4 94.1	94.3	7.6 7.6	7.6	7.6	3.4 3.5	3.5	3.6	4.5 2.9	3.7	3.5
					Middle	5.1	16.1 16.1	16.1	8.1 8.1	8.1	33.2 33.3	33.3	94.0 93.7	93.9	7.6 7.5	7.6		3.5 3.7	3.6		4.0 3.6	3.8	
					Bottom	9.2	16.2 16.1	16.2	8.0 8.1	8.1	33.5 33.4	33.5	94.3 93.9	94.1	7.6 7.6	7.6		3.5 3.6	3.6		3.0 3.1	3.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	18:40	34.5	Surface	1.0	20.7 20.7	20.7	8.2 8.2	8.2	23.5 23.7	23.6	92.1 91.7	91.9	7.1 7.1	7.1	7.1	2.8 2.6	2.7	2.8	5.0 4.2	4.6	4.5
					Middle	17.3	20.7 20.7	20.7	8.2 8.2	8.2	25.2 25.1	25.1	91.9 90.5	91.2	7.0 7.1	7.1		2.8 2.8	2.8		4.5 4.4	4.5	
					Bottom	33.5	20.7 20.7	20.7	8.2 8.2	8.2	26.7 27.0	26.9	89.5 90.1	89.8	6.9 7.0	6.9		2.9 2.9	2.9		4.2 4.4	4.3	
4-Dec-15	Cloudy	Moderate	04:50	34.2	Surface	1.0	19.3 19.4	19.4	8.1 8.1	8.1	30.2 30.3	30.3	95.5 95.1	95.3	7.4 7.3	7.3	7.3	1.2 1.4	1.3	1.5	3.1 2.6	2.9	2.7
					Middle	17.1	20.0 20.1	20.0	8.1 8.1	8.1	31.4 31.7	31.6	93.6 93.9	93.8	7.2 7.3	7.3		1.4 1.6	1.5		2.5 2.5	2.5	
					Bottom	33.2	20.0 20.0	20.0	8.2 8.1	8.1	33.2 33.9	33.6	92.0 92.8	92.4	7.1 7.1	7.1		1.6 1.6	1.6		2.5 3.1	2.8	
7-Dec-15	Cloudy	Moderate	08:36	34.3	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	35.8 35.9	35.9	94.4 94.6	94.5	7.0 7.0	7.0	7.0	2.1 2.1	2.1	2.3	4.1 4.5	4.3	4.3
					Middle	17.2	19.5 19.5	19.5	8.2 8.2	8.2	36.0 35.8	35.9	93.3 94.1	93.7	6.9 7.0	7.0		2.3 2.3	2.3		5.1 3.6	4.4	
					Bottom	33.3	19.5 19.5	19.5	8.2 8.2	8.2	35.7 36.0	35.8	92.3 92.5	92.4	6.9 6.9	6.9		2.3 2.4	2.4		4.9 3.3	4.1	
9-Dec-15	Rainy	Moderate	10:08	36.3	Surface	1.0	19.1 19.1	19.1	8.2 8.2	8.2	36.2 36.2	36.2	95.2 92.6	93.9	7.1 6.9	7.0	7.0	3.1 3.2	3.2	3.3	3.8 3.2	3.5	3.2
					Middle	18.2	19.1 19.1	19.1	8.2 8.2	8.2	36.3 36.3	36.3	93.6 92.1	92.9	7.0 6.9	6.9		3.1 3.2	3.2		3.0 3.5	3.3	
					Bottom	35.3	19.1 19.1	19.1	8.2 8.2	8.2	36.3 36.3	36.3	93.4 92.0	92.7	7.0 6.9	6.9		3.3 3.4	3.4		2.7 3.1	2.9	
11-Dec-15	Sunny	Moderate	13:49	33.3	Surface	1.0	18.9 18.8	18.9	8.2 8.2	8.2	29.4 29.6	29.5	89.3 89.3	89.3	7.0 7.0	7.0	7.0	4.5 4.7	4.6	5.1	3.2 3.7	3.5	4.5
					Middle	16.7	18.8 18.8	18.8	8.2 8.2	8.2	29.5 29.4	29.4	89.3 89.2	89.3	7.0 7.0	7.0		5.6 5.2	5.4		4.1 5.2	4.7	
					Bottom	32.3	18.8 18.8	18.8	8.2 8.2	8.2	29.5 29.4	29.4	88.3 89.0	88.7	6.9 7.0	6.9		5.3 5.2	5.3		4.4 6.1	5.3	
14-Dec-15	Rainy	Moderate	16:00	34.4	Surface	1.0	18.5 18.5	18.5	8.1 8.2	8.2	27.0 27.5	27.2	91.5 91.6	91.6	7.3 7.3	7.3	7.3	4.6 4.5	4.6	4.8	6.6 6.6	6.6	5.5
					Middle	17.2	18.5 18.5	18.5	8.1 8.1	8.1	27.7 27.5	27.6	91.5 91.1	91.3	7.3 7.2	7.3		4.8 4.7	4.8		5.7 4.6	5.2	
					Bottom	33.4	18.5 18.5	18.5	8.1 8.1	8.1	27.5 27.6	27.6	90.4 90.8	90.6	7.2 7.2	7.2		5.0 4.9	5.0		4.8 4.6	4.7	
16-Dec-15	Sunny	Moderate	17:32	34.2	Surface	1.0	18.1 18.1	18.1	8.2 8.2	8.2	30.5 30.7	30.6	90.6 91.3	91.0	7.1 7.2	7.1	7.1	1.8 1.7	1.8	2.0	6.4 7.3	6.9	7.9
					Middle	17.1	18.1 18.1	18.1	8.2 8.2	8.2	30.9 30.8	30.8	91.2 89.2	90.2	7.2 7.0	7.1		2.1 2.1	2.1		8.3 8.1	8.2	
					Bottom	33.2	18.1 18.1	18.1	8.2 8.2	8.2	30.9 31.0	31.0	89.1 89.7	89.4	7.0 7.1	7.0		2.1 2.1	2.1		8.4 8.8	8.6	
18-Dec-15	Sunny	Moderate	13:58	35.6	Surface	1.0	17.3 17.4	17.4	8.2 8.2	8.2	29.0 29.1	29.1	93.6 93.7	93.7	7.5 7.6	7.5	7.5	4.4 4.5	4.5	4.5	6.2 5.8	6.0	6.1
					Middle	17.8	17.3 17.3	17.3	8.2 8.2	8.2	29.2 29.1	29.1	94.4 92.8	93.6	7.6 7.5	7.5		5.3 4.9	5.1		5.9 6.6	6.3	
					Bottom	34.6	17.3 17.3	17.3	8.2 8.2	8.2	29.2 29.1	29.2	95.6 94.4	95.0	7.7 7.6	7.7		4.0 4.0	4.0		5.7 6.4	6.1	
21-Dec-15	Cloudy	Moderate	08:03	34.4	Surface	1.0	16.9 16.8	16.9	8.1 8.1	8.1	36.1 35.9	36.0	91.5 92.2	91.9	7.1 7.2	7.2	7.2	3.4 3.5	3.5	3.6	5.4 4.2	4.8	4.5
					Middle	17.2	16.8 16.8	16.8	8.1 8.1	8.1	35.9 36.1	36.0	92.1 91.3	91.7	7.2 7.1	7.2		3.8 3.6	3.7		3.4 5.0	4.2	
					Bottom	33.4	16.8 16.9	16.9	8.1 8.2	8.1	36.0 35.8	35.9	91.3 92.0	91.7	7.1 7.2	7.2		3.6 3.8	3.7		5.1 3.7	4.4	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	09:36	34.7	Surface	1.0	16.8 16.8	16.8	8.1 8.1	8.1	35.4 35.3	35.3	91.4 90.6	91.0	7.2 7.1	7.1	7.1	2.8 2.7	2.8	3.1	4.6 4.6	4.6	4.6
					Middle	17.4	16.8 16.8	16.8	8.1 8.1	8.1	35.7 35.5	35.6	90.5 90.2	90.4	7.1 7.1	7.1		3.1 3.2	3.2		5.0 5.3	5.2	
					Bottom	33.7	16.8 16.8	16.8	8.1 8.0	8.1	35.7 35.3	35.5	88.0 88.0	88.0	6.9 6.9	6.9		3.4 3.4	3.4		3.6 4.6	4.1	
25-Dec-15	Cloudy	Moderate	13:34	36.1	Surface	1.0	16.7 16.8	16.8	8.1 8.1	8.1	26.4 25.8	26.1	96.2 94.8	95.5	7.8 7.8	7.8	7.8	5.4 5.5	5.5	5.5	5.2 6.0	5.6	5.5
					Middle	18.1	16.9 16.9	16.9	8.1 8.1	8.1	27.9 27.8	27.9	95.1 94.4	94.8	7.8 7.8	7.8		5.4 5.5	5.5		4.7 4.5	4.6	
					Bottom	35.1	16.9 16.9	16.9	8.1 8.1	8.1	28.7 27.9	28.3	94.6 93.8	94.2	7.8 7.7	7.8		5.5 5.5	5.5		6.3 6.1	6.2	
28-Dec-15	Sunny	Moderate	15:42	34.6	Surface	1.0	16.4 16.4	16.4	8.2 8.2	8.2	26.9 26.8	26.9	92.7 92.7	92.7	7.7 7.7	7.7	7.7	2.7 2.7	2.7	3.0	4.3 5.8	5.1	5.0
					Middle	17.3	16.4 16.4	16.4	8.1 8.2	8.2	26.9 27.0	26.9	92.0 92.5	92.3	7.7 7.7	7.7		2.9 2.9	2.9		6.0 5.5	5.8	
					Bottom	33.6	16.4 16.4	16.4	8.2 8.1	8.1	27.0 26.8	26.9	91.9 91.7	91.8	7.6 7.6	7.6		3.2 3.3	3.3		4.2 3.8	4.0	
30-Dec-15	Cloudy	Moderate	17:21	34.0	Surface	1.0	16.3 16.3	16.3	8.2 8.2	8.2	28.2 28.2	28.2	92.7 91.2	92.0	7.7 7.5	7.6	7.6	2.6 2.6	2.6	3.1	2.5 2.1	2.3	3.3
					Middle	17.0	16.3 16.3	16.3	8.2 8.2	8.2	28.3 28.4	28.4	92.3 92.3	92.3	7.6 7.6	7.6		3.3 3.4	3.4		2.0 2.4	2.2	
					Bottom	33.0	16.3 16.3	16.3	8.2 8.2	8.2	28.4 28.3	28.4	92.7 92.6	92.7	7.7 7.7	7.7		3.4 3.4	3.4		5.7 5.2	5.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	11:40	34.5	Surface	1.0	20.6 20.6	20.6	8.1 8.1	8.1	28.9 29.0	29.0	95.8 96.0	95.9	7.3 7.3	7.3	7.3	1.9 1.9	1.9	2.1	2.9 3.7	3.3	3.5
					Middle	17.3	20.5 20.4	20.5	8.1 8.1	8.1	29.0 29.4	29.2	94.2 95.4	94.8	7.2 7.2	7.2		2.1 2.2	2.2		3.9 3.2	3.6	
					Bottom	33.5	20.4 20.5	20.4	8.1 8.1	8.1	29.5 29.3	29.4	92.8 92.9	92.9	7.0 7.1	7.0		2.2 2.2	2.2		3.0 4.0	3.5	
4-Dec-15	Cloudy	Moderate	16:05	34.4	Surface	1.0	19.7 19.6	19.7	8.2 8.2	8.2	25.4 25.6	25.5	92.2 94.9	93.6	7.3 7.3	7.3	7.3	2.1 2.2	2.2	2.3	4.4 3.4	3.9	3.8
					Middle	17.2	20.1 20.3	20.2	8.2 8.2	8.2	25.9 27.7	26.8	94.9 91.9	93.4	7.3 7.2	7.3		2.3 2.3	2.3		3.7 4.4	3.7	
					Bottom	33.4	20.3 20.2	20.3	8.2 8.2	8.2	27.9 28.1	28.0	92.2 91.4	91.8	7.1 7.1	7.1		2.5 2.5	2.5		3.7 3.9	3.8	
7-Dec-15	Cloudy	Moderate	17:43	34.3	Surface	1.0	19.6 19.6	19.6	8.3 8.3	8.3	30.6 30.6	30.6	93.4 93.9	93.7	7.2 7.2	7.2	7.2	3.4 3.4	3.4	3.5	4.0 3.3	3.7	3.7
					Middle	17.2	19.6 19.6	19.6	8.3 8.3	8.3	30.6 30.6	30.6	92.6 92.5	92.6	7.1 7.1	7.1		3.5 3.4	3.5		3.9 2.9	3.4	
					Bottom	33.3	19.6 19.6	19.6	8.3 8.3	8.3	30.6 30.7	30.7	92.5 91.9	92.2	7.1 7.0	7.1		3.6 3.6	3.6		2.7 5.0	3.9	
9-Dec-15	Rainy	Moderate	18:14	36.1	Surface	1.0	19.1 19.1	19.1	8.2 8.2	8.2	30.0 29.9	30.0	90.8 90.9	90.9	7.0 7.1	7.0	7.0	5.2 5.3	5.3	5.5	4.2 4.6	4.4	5.7
					Middle	18.1	19.1 19.1	19.1	8.2 8.2	8.2	29.9 30.0	30.0	90.9 90.6	90.8	7.1 7.0	7.0		5.5 5.4	5.5		6.7 6.3	6.5	
					Bottom	35.1	19.1 19.1	19.1	8.2 8.2	8.2	30.0 29.9	29.9	90.6 90.0	90.3	7.0 7.0	7.0		5.6 5.5	5.6		6.0 6.6	6.3	
11-Dec-15	Sunny	Moderate	06:33	34.6	Surface	1.0	18.8 18.8	18.8	8.1 8.0	8.0	36.1 35.9	36.0	90.3 93.2	91.8	6.8 7.0	6.9	6.9	7.6 7.5	7.6	7.5	9.7 10.2	10.0	10.1
					Middle	17.3	18.8 18.8	18.8	8.0 8.0	8.0	36.1 35.8	35.9	90.2 91.5	90.9	6.8 6.9	6.8		7.5 7.5	7.5		10.7 10.2	10.5	
					Bottom	33.6	18.8 18.8	18.8	7.9 8.0	8.0	35.5 36.0	35.8	91.1 90.0	90.6	6.9 6.8	6.8		7.5 7.4	7.5		9.6 10.2	9.9	
14-Dec-15	Rainy	Moderate	08:39	34.4	Surface	1.0	18.3 18.3	18.3	8.1 8.1	8.1	33.0 33.2	33.1	94.0 94.0	94.0	7.2 7.2	7.2	7.2	4.8 4.8	4.8	5.1	7.1 5.5	6.3	6.3
					Middle	17.2	18.4 18.4	18.4	8.1 8.1	8.1	33.8 33.6	33.7	92.3 92.5	92.4	7.1 7.1	7.1		5.1 5.0	5.1		5.2 6.5	5.9	
					Bottom	33.4	18.4 18.4	18.4	8.1 8.1	8.1	34.0 33.7	33.9	91.8 91.8	91.8	7.1 7.1	7.1		5.3 5.2	5.3		6.1 7.1	6.6	
16-Dec-15	Sunny	Moderate	10:16	34.6	Surface	1.0	17.7 17.7	17.7	8.0 8.0	8.0	33.5 33.5	33.5	93.3 93.7	93.5	7.3 7.3	7.3	7.3	3.9 4.1	4.0	3.9	7.2 6.9	7.1	7.4
					Middle	17.3	17.8 17.7	17.7	8.0 8.0	8.0	33.6 33.5	33.6	91.1 92.8	92.0	7.1 7.2	7.2		3.8 3.7	3.8		8.2 7.1	7.7	
					Bottom	33.6	17.7 17.7	17.7	8.0 7.9	8.0	33.7 33.5	33.6	90.8 91.7	91.3	7.1 7.2	7.1		3.9 3.8	3.9		7.4 7.2	7.3	
18-Dec-15	Cloudy	Moderate	04:22	35.3	Surface	1.0	16.9 16.9	16.9	8.0 8.0	8.0	35.1 35.3	35.2	95.6 93.0	94.3	7.5 7.3	7.4	7.5	5.2 5.7	5.5	5.6	6.1 6.2	6.2	5.5
					Middle	17.7	16.9 17.0	17.0	8.0 8.0	8.0	35.2 35.5	35.4	97.2 93.9	95.6	7.6 7.3	7.5		5.6 5.5	5.6		5.6 5.9	5.8	
					Bottom	34.3	16.9 17.0	16.9	8.0 8.0	8.0	35.1 35.4	35.3	99.0 93.7	96.4	7.8 7.3	7.5		5.4 5.7	5.6		4.2 4.6	4.4	
21-Dec-15	Sunny	Moderate	16:27	34.7	Surface	1.0	16.9 16.9	16.9	8.2 8.2	8.2	29.2 28.8	29.0	91.8 91.7	91.8	7.5 7.5	7.5	7.5	2.9 2.9	2.9	2.9	5.5 6.0	5.8	5.3
					Middle	17.4	16.9 16.9	16.9	8.2 8.2	8.2	28.9 32.3	30.6	91.5 91.1	91.3	7.5 7.4	7.4		2.8 2.9	2.9		5.0 5.4	5.2	
					Bottom	33.7	16.9 16.9	16.9	8.2 8.2	8.2	28.9 28.8	28.9	91.5 90.1	90.8	7.4 7.3	7.4		2.9 2.9	2.9		4.8 5.1	5.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	18:25	34.9	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	25.8 26.8	26.3	94.6 94.8	94.7	7.8 7.8	7.8	7.8	2.3 2.4	2.4	2.5	3.1 2.2	2.7	3.2
					Middle	17.5	16.7 16.7	16.7	8.1 8.1	8.1	26.7 26.6	26.6	93.5 93.1	93.3	7.7 7.8	7.7		2.6 2.5	2.6		4.0 3.0	3.5	
					Bottom	33.9	16.8 16.7	16.8	8.1 8.1	8.1	26.8 26.5	26.7	92.4 93.0	92.7	7.6 7.7	7.7		2.6 2.5	2.6		3.1 3.6	3.4	
25-Dec-15	Cloudy	Moderate	06:43	36.2	Surface	1.0	16.9 16.9	16.9	8.0 8.0	8.0	33.8 33.8	33.8	91.5 98.4	95.0	7.2 7.8	7.5	7.4	7.4 7.4	7.4	7.6	10.2 11.1	10.7	10.9
					Middle	18.1	16.9 16.9	16.9	8.0 8.0	8.0	33.8 33.9	33.9	89.3 93.1	91.2	7.1 7.4	7.2		7.6 7.6	7.6		11.3 10.6	11.0	
					Bottom	35.2	16.9 16.9	16.9	8.0 8.0	8.0	33.8 33.9	33.9	89.2 89.7	89.5	7.1 7.1	7.1		7.6 7.7	7.7		10.6 11.2	10.9	
28-Dec-15	Sunny	Moderate	08:44	34.8	Surface	1.0	16.1 16.1	16.1	7.9 8.0	8.0	31.7 31.9	31.8	95.2 96.0	95.6	7.8 7.8	7.8	7.8	5.8 5.7	5.8	6.0	7.8 7.2	7.5	7.4
					Middle	17.4	16.1 16.1	16.1	7.9 8.0	7.9	31.6 31.9	31.7	94.5 95.1	94.8	7.7 7.7	7.7		6.1 6.1	6.1		6.9 7.8	7.4	
					Bottom	33.8	16.1 16.1	16.1	7.9 8.0	7.9	31.5 32.0	31.8	94.3 94.3	94.3	7.7 7.6	7.6		6.1 6.2	6.2		7.0 7.6	7.3	
30-Dec-15	Cloudy	Moderate	10:01	34.1	Surface	1.0	16.1 16.1	16.1	8.0 8.0	8.0	33.0 33.1	33.1	94.4 92.0	93.2	7.6 7.4	7.5	7.5	3.3 3.4	3.4	3.5	3.2 4.9	4.1	3.3
					Middle	17.1	16.2 16.2	16.2	8.0 8.0	8.0	33.5 33.5	33.5	93.1 92.1	92.6	7.5 7.4	7.4		3.4 3.5	3.5		3.0 2.6	2.8	
					Bottom	33.1	16.2 16.2	16.2	8.0 8.0	8.0	33.4 33.4	33.4	93.9 94.3	94.1	7.5 7.6	7.6		3.4 3.5	3.5		2.3 3.6	3.0	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:00	3.2	Surface	1.0	24.0 24.0	24.0	8.1 8.1	8.1	27.5 27.7	27.6	93.9 90.1	92.0	6.8 6.5	6.6	6.6	7.5 7.8	7.7	7.7	5.3 4.6	5.0	5.5
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-		
					Bottom	2.2	23.9 23.8	23.8	8.1 8.1	8.1	27.7 27.7	27.7	93.8 91.7	92.8	6.8 6.6	6.7		7.8 7.4	7.6		5.7 6.3	6.0	
4-Dec-15	Cloudy	Moderate	07:14	3.0	Surface	1.0	22.5 22.7	22.6	8.1 8.1	8.1	24.9 24.7	24.8	92.0 92.9	92.5	6.9 7.0	6.9	6.9	5.6 5.5	5.6	5.6	4.9 4.7	4.8	4.5
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-				
					Bottom	2.0	22.5 22.8	22.7	8.1 8.1	8.1	25.0 25.2	25.1	92.6 96.0	94.3	6.9 7.2	7.0		5.6 5.5	5.6		3.9 4.5	4.2	
7-Dec-15	Cloudy	Moderate	11:05	3.2	Surface	1.0	22.1 22.1	22.1	8.2 8.2	8.2	29.1 29.0	29.1	84.2 88.4	86.3	6.2 6.5	6.4	6.4	5.7 5.5	5.6	5.6	3.5 4.8	4.2	4.3
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-				
					Bottom	2.2	22.2 22.3	22.2	8.2 8.2	8.2	29.2 29.3	29.3	86.5 83.8	85.2	6.4 6.2	6.3		5.6 5.6	5.6		5.3 3.2	4.3	
9-Dec-15	Rainy	Moderate	12:38	3.2	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	29.9 29.9	29.9	91.7 87.6	89.7	6.8 6.5	6.6	6.6	5.7 5.9	5.8	5.8	3.7 4.1	3.9	4.0
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.2	21.6 21.6	21.6	8.2 8.2	8.2	29.9 29.9	29.9	89.8 96.7	93.3	6.6 7.2	6.9		5.8 5.8	5.8		3.8 4.2	4.0	
11-Dec-15	Sunny	Moderate	11:50	3.3	Surface	1.0	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	86.1 88.9	87.5	6.4 6.6	6.5	6.5	7.3 7.1	7.2	7.1	7.1 6.4	6.8	6.3
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.3	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	91.8 87.1	89.5	6.8 6.5	6.6		6.7 7.3	7.0		5.8 5.8	5.8	
14-Dec-15	Rainy	Moderate	14:05	3.3	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.0 30.1	30.1	90.4 90.6	90.5	6.7 6.7	6.7	6.7	6.5 6.4	6.5	6.6	8.8 9.8	9.3	10.0
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.3	21.6 21.6	21.6	8.2 8.2	8.2	30.0 30.1	30.0	91.3 90.8	91.1	6.8 6.7	6.7		6.6 6.6	6.6		11.5 9.8	10.7	
16-Dec-15	Sunny	Moderate	15:31	3.3	Surface	1.0	20.4 20.4	20.4	8.2 8.2	8.2	26.6 26.6	26.6	90.7 90.2	90.5	7.0 7.0	7.0	7.0	8.0 8.4	8.2	8.3	10.7 9.5	10.1	11.2
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.3	20.4 20.4	20.4	8.2 8.2	8.2	26.6 26.6	26.6	94.5 90.6	92.6	7.3 7.0	7.1		8.3 8.4	8.4		13.1 11.4	12.3	
18-Dec-15	Sunny	Moderate	11:47	3.1	Surface	1.0	18.9 18.9	18.9	8.2 8.2	8.2	28.7 28.7	28.7	94.9 93.1	94.0	7.4 7.3	7.4	7.4	6.0 5.9	6.0	5.9	7.7 7.4	7.6	7.5
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.1	18.9 18.7	18.8	8.2 8.2	8.2	28.7 28.7	28.7	93.1 96.5	94.8	7.3 7.6	7.4		6.0 5.6	5.8		7.3 7.4	7.4	
21-Dec-15	Cloudy	Moderate	14:19	3.1	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	29.6 29.7	29.6	93.0 93.7	93.4	7.2 7.3	7.2	7.2	7.6 7.5	7.6	7.7	5.1 5.1	5.1	4.5
					Middle	-	-	-	-	-	-	-	-	-	-	-		-					
					Bottom	2.1	19.3 19.3	19.3	8.2 8.2	8.2	29.7 29.6	29.6	92.5 93.1	92.8	7.2 7.2	7.2		7.8 7.7	7.8		3.1 4.5	3.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	12:01	3.2	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.9 29.9	29.9	92.0 90.5	91.3	7.1 6.9	7.0	7.0	8.6 8.6	8.6	8.7	8.5 8.3	8.4	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	19.7 19.7	19.7	8.2 8.2	8.2	29.9 30.1	30.0	91.8 94.0	92.9	7.0 7.2	7.1		7.1	8.8 8.6		8.7	7.1		7.0 6.5	6.8	7.0 6.5
25-Dec-15	Cloudy	Moderate	11:59	3.3	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	28.4 28.4	28.4	96.5 94.6	95.6	7.4 7.2	7.3	7.3	3.6 3.6	3.6	3.7	3.7 3.9	3.8	3.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	20.2 20.2	20.2	8.2 8.2	8.2	28.4 28.4	28.4	95.6 97.4	96.5	7.3 7.5	7.4		7.4	3.7 3.6		3.7	7.4		3.0 4.4	3.7	3.0 4.4
28-Dec-15	Sunny	Moderate	13:53	3.2	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.1 28.1	28.1	89.1 90.3	89.7	7.0 7.1	7.0	7.0	6.3 6.4	6.4	6.5	9.3 9.0	9.2	8.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	19.3 19.3	19.3	8.2 8.2	8.2	28.1 28.1	28.1	95.1 90.5	92.8	7.4 7.1	7.3		7.3	6.4 6.5		6.5	7.3		8.9 8.2	8.6	8.9 8.2
30-Dec-15	Cloudy	Moderate	14:52	3.4	Surface	1.0	19.3 19.3	19.3	8.3 8.2	8.3	28.8 28.8	28.8	93.2 91.0	92.1	7.3 7.1	7.2	7.2	5.8 6.1	6.0	5.7	6.5 6.2	6.4	6.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	19.3 19.3	19.3	8.3 8.2	8.3	28.8 28.8	28.8	95.4 93.1	94.3	7.4 7.2	7.3		7.3	5.2 5.5		5.4	7.3		6.3 6.1	6.2	6.3 6.1

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
2-Dec-15	Sunny	Moderate	12:58	3.2	Surface	1.0	23.7 23.7	23.7	8.1 8.1	8.1	25.4 25.4	25.4	96.6 95.6	96.1 7.0	7.0	7.0	10.6 11.2	10.9	11.0	7.8 7.0	7.4	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	23.7 23.7	23.7	8.1 8.1	8.1	25.6 25.6	25.6	97.1 95.9	96.5	7.1 7.0		7.1	10.6 11.3		11.0	7.1		10.6 11.3	11.0	8.5 6.9
4-Dec-15	Cloudy	Moderate	13:18	3.1	Surface	1.0	22.5 22.5	22.5	8.1 8.1	8.1	26.3 26.3	26.3	94.5 93.8	94.2 7.0	7.0	7.0	4.2 4.2	4.2	4.3	4.7 5.4	5.1	4.9			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	22.5 22.6	22.5	8.1 8.1	8.1	26.3 26.4	26.3	98.6 94.7	96.7	7.3 7.0		7.2	4.4 4.2		4.3	7.2		4.4 4.2	4.3	4.7 4.6
7-Dec-15	Cloudy	Moderate	15:19	3.2	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	30.2 30.1	30.2	92.7 93.7	93.2 6.8	6.8	6.8	5.2 5.3	5.3	5.3	6.8 6.8	6.8	7.4			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	22.3 22.3	22.3	8.2 8.2	8.2	30.2 30.1	30.2	93.2 95.3	94.3	6.8 7.0		6.9	5.3 5.3		5.3	6.9		5.3 5.3	5.3	7.5 8.3
9-Dec-15	Rainy	Moderate	16:08	3.3	Surface	1.0	21.3 21.3	21.3	8.1 8.1	8.1	28.8 28.7	28.7	88.4 89.9	89.2 6.6	6.7	6.7	4.6 4.7	4.7	4.7	4.9 4.7	4.8	4.8			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	21.3 21.4	21.3	8.1 8.1	8.1	28.8 28.8	28.8	89.0 92.8	90.9	6.7 7.0		6.8	4.6 4.6		4.6	6.8		4.6 4.6	4.6	5.0 4.5
11-Dec-15	Sunny	Moderate	08:21	3.2	Surface	1.0	21.2 21.2	21.2	8.2 8.2	8.2	30.4 30.3	30.3	89.1 93.2	91.2 6.6	6.8	6.8	5.9 6.0	6.0	6.1	4.5 4.8	4.7	4.5			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	21.2 21.2	21.2	8.2 8.2	8.2	30.4 30.4	30.4	97.2 90.7	94.0	7.2 6.8		7.0	6.3 6.1		6.2	7.0		6.3 6.1	6.2	4.5 4.0
14-Dec-15	Rainy	Moderate	10:37	3.1	Surface	1.0	21.5 21.6	21.6	8.2 8.2	8.2	30.0 30.0	30.0	92.2 90.5	91.4 6.8	6.8	6.8	8.6 8.8	8.7	8.6	9.2 9.5	9.4	10.3			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	21.6 21.5	21.5	8.2 8.2	8.2	30.0 29.9	30.0	91.2 94.5	92.9	6.8 7.0		6.9	8.5 8.5		8.5	6.9		8.5 8.5	8.5	10.3 11.8
16-Dec-15	Sunny	Moderate	12:07	3.3	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.4	27.4	88.5 88.7	88.1 6.8	6.8	6.8	6.2 6.6	6.4	6.4	10.9 10.3	10.6	10.6			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.4	27.4	91.5 88.1	89.8	7.0 6.8		6.9	6.1 6.7		6.4	6.9		6.1 6.7	6.4	10.3 10.7
18-Dec-15	Cloudy	Moderate	06:11	3.3	Surface	1.0	19.0 19.0	19.0	8.2 8.2	8.2	28.5 28.5	28.5	89.3 89.1	89.2 7.0	7.0	7.0	6.8 7.0	6.9	6.8	5.8 6.1	6.0	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	19.0 19.1	19.1	8.2 8.2	8.2	28.6 28.7	28.7	89.3 89.5	89.4	7.0 7.0		7.0	6.8 6.5		6.7	7.0		6.8 6.5	6.7	4.5 4.3
21-Dec-15	Sunny	Moderate	10:02	3.2	Surface	1.0	19.0 19.0	19.0	8.2 8.2	8.2	30.0 30.0	30.0	86.7 87.4	87.1 6.7	6.8	6.8	5.4 5.0	5.2	6.0	9.9 11.4	10.7	11.8			
					Middle	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	18.9 19.0	19.0	8.2 8.2	8.2	30.0 30.1	30.1	87.3 86.9	87.1	6.8 6.7		6.8	6.6 6.8		6.7	6.8		6.6 6.8	6.7	11.9 13.8

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-Dec-15	Sunny	Moderate	15:51	3.2	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.3 30.3	30.3	95.8 93.4	94.6	7.3 7.1	7.2	7.2	7.8 7.7	7.8	7.8	7.7 8.7	8.2	8.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	20.3 20.3	20.3	8.2 8.2	8.2	30.5 30.4	30.4	91.2 94.5	92.9	6.9 7.2	7.0		7.0	7.8 7.8		7.8	7.0		7.8 7.8	7.8	8.5 8.2	8.4
25-Dec-15	Cloudy	Moderate	08:24	3.4	Surface	1.0	20.3 20.3	20.3	8.1 8.1	8.1	28.4 28.3	28.4	93.8 95.4	94.6	7.2 7.3	7.2	7.2	5.4 5.2	5.3	5.4	5.5 5.7	5.6	5.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.4	20.3 20.3	20.3	8.1 8.1	8.1	28.4 28.4	28.4	95.8 93.5	94.7	7.3 7.2	7.2		7.2	5.4 5.4		5.4	7.2		5.4 5.4	5.4	6.2 4.6	5.4
28-Dec-15	Sunny	Moderate	10:37	3.1	Surface	1.0	19.2 19.2	19.2	8.2 8.2	8.2	28.0 28.0	28.0	90.7 89.1	89.9	7.1 7.0	7.0	7.0	8.7 8.9	8.8	8.8	11.9 11.1	11.5	11.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	19.2 19.2	19.2	8.2 8.2	8.2	28.0 27.9	28.0	89.5 96.4	93.0	7.0 7.6	7.3		7.3	8.9 8.5		8.7	7.3		8.9 8.5	8.7	12.5 12.1	12.3
30-Dec-15	Cloudy	Moderate	11:51	3.2	Surface	1.0	19.2 19.2	19.2	8.2 8.2	8.2	28.2 28.1	28.2	91.0 92.4	91.7	7.1 7.2	7.2	7.2	8.5 8.6	8.6	8.6	10.1 9.6	9.9	9.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	19.2 19.2	19.2	8.2 8.2	8.2	28.2 28.1	28.2	91.6 95.0	93.3	7.2 7.4	7.3		7.3	8.5 8.5		8.5	7.3		8.5 8.5	8.5	9.6 9.2	9.4

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	17:19	3.7	Surface	1.0	24.1 24.1	24.1	8.1 8.1	8.1	27.5 27.5	27.5	89.6 89.5	89.6	6.4 6.4	6.4	6.4	9.3 8.8	9.1	9.0	10.1 9.9	10.0	10.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	24.0 24.0	24.0	8.1 8.1	8.1	27.6 27.7	27.7	89.5 89.8	89.7	6.4 6.5	6.5		6.5	8.9 8.9		8.9	11.0 10.3		10.7		
4-Dec-15	Cloudy	Moderate	07:01	3.6	Surface	1.0	22.7 22.7	22.7	8.1 8.1	8.1	24.7 24.7	24.7	88.1 90.4	89.3	6.6 6.8	6.7	6.7	5.7 5.7	5.7	5.8	3.0 3.5	3.3	4.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	23.0 23.1	23.1	8.1 8.1	8.1	27.8 27.9	27.9	90.9 95.9	93.4	6.6 7.0	6.8		6.8	5.8 5.8		5.8	5.1 4.5		4.8		
7-Dec-15	Cloudy	Moderate	10:49	3.6	Surface	1.0	21.7 21.8	21.8	8.1 8.1	8.1	28.7 28.8	28.7	95.7 92.7	94.2	7.1 6.9	7.0	7.0	3.5 3.6	3.6	3.7	4.3 5.1	4.7	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	21.7 21.9	21.8	8.1 8.1	8.1	28.9 28.8	28.9	94.6 100.2	97.4	7.0 7.4	7.2		7.2	3.7 3.6		3.7	4.7 3.1		3.9		
9-Dec-15	Rainy	Moderate	12:21	3.8	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	29.8 29.9	29.9	90.3 91.5	90.9	6.7 6.8	6.7	6.7	4.5 4.1	4.3	4.4	4.4 4.0	4.2	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.8	21.5 21.5	21.5	8.2 8.2	8.2	29.8 29.9	29.8	92.7 89.2	91.0	6.9 6.6	6.8		6.8	4.5 4.3		4.4	4.4 4.1		4.3		
11-Dec-15	Sunny	Moderate	12:08	3.6	Surface	1.0	21.7 21.7	21.7	8.2 8.2	8.2	30.7 30.6	30.6	87.5 88.9	88.2	6.4 6.5	6.5	6.5	4.5 4.7	4.6	4.6	4.6 3.5	4.1	4.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.6	21.7 21.7	21.7	8.2 8.2	8.2	30.7 30.7	30.7	88.2 90.6	89.4	6.5 6.7	6.6		6.6	4.6 4.5		4.6	4.7 4.9		4.8		
14-Dec-15	Rainy	Moderate	14:20	3.7	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	28.8 28.7	28.8	91.0 89.8	90.4	6.8 6.7	6.7	6.7	5.4 5.5	5.5	5.5	5.7 5.5	5.6	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.7	21.5 21.5	21.5	8.2 8.2	8.2	29.4 29.0	29.2	91.9 90.6	91.3	6.8 6.8	6.8		6.8	5.5 5.5		5.5	6.0 5.2		5.6		
16-Dec-15	Sunny	Moderate	15:48	3.5	Surface	1.0	20.6 20.7	20.7	8.1 8.1	8.1	27.0 27.0	27.0	100.2 94.7	97.5	7.7 7.3	7.5	7.5	6.4 6.5	6.5	6.4	10.3 9.8	10.1	10.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.5	20.6 20.7	20.6	8.1 8.1	8.1	27.0 27.0	27.0	102.1 95.2	98.7	7.8 7.3	7.6		7.6	6.0 6.5		6.3	10.8 10.5		10.7		
18-Dec-15	Sunny	Moderate	12:04	3.8	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.8 28.8	28.8	91.4 92.6	92.0	7.1 7.2	7.2	7.2	8.1 8.2	8.2	8.2	4.7 3.3	4.0	3.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.8	19.3 19.4	19.4	8.2 8.2	8.2	28.9 29.1	29.0	91.8 95.1	93.5	7.1 7.4	7.2		7.2	8.1 8.1		8.1	3.3 3.7		3.5		
21-Dec-15	Cloudy	Moderate	14:36	3.2	Surface	1.0	19.6 19.5	19.6	8.2 8.2	8.2	29.7 29.7	29.7	89.8 90.0	89.9	6.9 6.9	6.9	6.9	7.3 7.1	7.2	7.2	8.8 7.1	8.0	7.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.2	19.5 19.5	19.5	8.2 8.2	8.2	29.8 29.8	29.8	90.9 89.6	90.3	7.0 6.9	7.0		7.0	7.3 6.9		7.1	5.5 6.7		6.1		

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	11:46	3.7	Surface	1.0	20.1 20.0	20.0	8.2 8.2	8.2	30.2 30.2	30.2	94.0 92.7	93.4	7.2 7.1	7.1	7.1	3.7 3.7	3.7	3.8	4.1 3.4	3.8	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	20.0 19.8	19.9	8.2 8.2	8.2	30.2 30.3	30.2	92.9 91.5	92.2	7.1 7.0	7.0		7.0	3.8 3.8		3.8	3.9 5.0		4.5		
25-Dec-15	Cloudy	Moderate	12:14	3.6	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	27.5 27.6	27.5	93.7 92.3	93.0	7.2 7.1	7.2	7.2	5.1 5.3	5.2	5.3	4.9 5.2	5.1	5.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	20.3 20.3	20.3	8.2 8.2	8.2	28.3 28.4	28.3	94.6 95.4	95.0	7.2 7.3	7.3		7.3	5.4 5.2		5.3	5.9 5.9		5.9		
28-Dec-15	Sunny	Moderate	14:07	3.8	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	93.6 91.3	92.5	7.3 7.1	7.2	7.2	4.7 4.7	4.7	4.7	6.6 6.7	6.7	6.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	19.4 19.4	19.4	8.2 8.2	8.2	28.1 28.1	28.1	92.5 90.4	91.5	7.2 7.0	7.1		7.1	4.7 4.7		4.7	6.2 5.9		6.1		
30-Dec-15	Cloudy	Moderate	15:10	3.6	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	28.7 28.7	28.7	91.9 93.3	92.6	7.1 7.2	7.2	7.2	4.3 4.3	4.3	4.4	4.7 4.0	4.4	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	19.7 19.7	19.7	8.2 8.2	8.2	28.7 28.7	28.7	95.9 92.2	94.1	7.4 7.1	7.3		7.3	4.5 4.3		4.4	6.7 5.0		5.9		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	12:45	3.6	Surface	1.0	23.9 23.8	23.8	8.1 8.1	8.1	25.9 25.9	25.9	87.6 88.5	88.1	6.4 6.4	6.4	6.4	21.9 21.7	21.8	21.9	21.1 21.6	21.4	23.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.6	23.8 23.8	23.8	8.1 8.1	8.1	26.0 26.0	26.0	87.0 88.3	87.7	6.3 6.4	6.4		21.4 22.3	21.9		25.1 23.8	24.5				
4-Dec-15	Cloudy	Moderate	13:33	3.4	Surface	1.0	22.9 22.9	22.9	8.1 8.1	8.1	26.8 26.8	26.8	92.5 87.8	90.2	6.8 6.5	6.6	6.6	8.8 8.9	8.9	8.8	8.1 7.1	7.6	8.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.4	22.9 22.9	22.9	8.1 8.1	8.1	26.8 26.8	26.8	92.3 88.6	90.5	6.8 6.5	6.7		8.8 8.6	8.7		8.2 8.3	8.3				
7-Dec-15	Cloudy	Moderate	15:34	3.7	Surface	1.0	22.2 22.3	22.2	8.2 8.2	8.2	29.9 29.9	29.9	91.8 87.7	89.8	6.7 6.4	6.6	6.6	3.9 3.7	3.8	3.8	3.8 4.3	4.1	4.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.7	22.5 22.3	22.4	8.1 8.2	8.2	30.2 30.0	30.1	91.0 89.5	90.3	6.6 6.6	6.6		3.8 3.8	3.8		5.0 5.7	5.4				
9-Dec-15	Rainy	Moderate	16:24	3.6	Surface	1.0	21.6 21.7	21.6	8.1 8.2	8.2	29.3 29.4	29.4	89.6 86.8	88.2	6.7 6.4	6.6	6.6	9.8 9.7	9.8	9.8	5.4 5.5	5.5	6.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.6	21.8 21.7	21.8	8.1 8.1	8.1	29.5 29.6	29.5	93.7 87.7	90.7	6.9 6.5	6.7		9.8 9.7	9.8		6.6 7.2	6.9				
11-Dec-15	Sunny	Moderate	08:03	3.5	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.6 30.7	30.7	92.7 92.2	92.5	6.8 6.8	6.8	6.8	5.9 6.0	6.0	6.2	7.1 7.1	7.1	6.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	2.5	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.7	30.7	86.3 87.6	87.0	6.4 6.5	6.4		6.4 6.2	6.3		6.5 5.8	6.2				
14-Dec-15	Rainy	Moderate	10:22	3.6	Surface	1.0	21.5 21.5	21.5	8.1 8.1	8.1	29.7 29.7	29.7	89.1 90.4	89.8	6.6 6.7	6.7	6.7	12.6 12.6	12.6	12.6	11.4 11.9	11.7	11.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	2.6	21.5 21.5	21.5	8.1 8.1	8.1	29.8 29.8	29.8	89.5 93.4	91.5	6.6 6.9	6.8		12.5 12.4	12.5		11.8 10.8	11.3				
16-Dec-15	Sunny	Moderate	11:53	3.5	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.4	27.4	91.2 88.9	90.1	7.0 6.8	6.9	6.9	7.5 7.2	7.4	7.9	10.0 10.6	10.3	10.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-					
					Bottom	2.5	20.5 20.5	20.5	8.1 8.1	8.1	27.5 27.5	27.5	91.7 88.4	90.1	7.0 6.8	6.9		8.1 8.4	8.3		10.8 10.7	10.8				
18-Dec-15	Cloudy	Moderate	05:57	3.7	Surface	1.0	19.5 19.7	19.6	8.2 8.2	8.2	28.5 28.7	28.6	86.9 86.8	86.9	6.7 6.7	6.7	6.7	4.2 4.3	4.3	4.3	4.9 5.6	5.3	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-					
					Bottom	2.7	19.6 20.0	19.8	8.2 8.2	8.2	29.9 29.7	29.8	87.8 88.0	87.9	6.7 6.7	6.7		4.2 4.2	4.2		5.7 4.6	5.2				
21-Dec-15	Sunny	Moderate	09:46	3.4	Surface	1.0	19.0 19.0	19.0	8.2 8.2	8.2	30.1 30.1	30.1	94.6 90.1	92.4	7.3 7.0	7.2	7.2	3.8 3.7	3.8	4.0	6.7 5.9	6.3	6.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-							
					Bottom	2.4	19.1 19.1	19.1	8.2 8.2	8.2	30.2 30.2	30.2	90.4 95.7	93.1	7.0 7.4	7.2		3.9 4.3	4.1		7.8 6.4	7.1				

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-Dec-15	Sunny	Moderate	16:05	3.7	Surface	1.0	20.4 20.3	20.4	8.2 8.2	8.2	30.5 30.6	30.6	94.0 92.8	93.4	7.1 7.0	7.0	7.0	5.2 5.3	5.3	5.4	7.7 7.1	7.4	8.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	20.3 20.2	20.3	8.2 8.2	8.2	30.6 30.6	30.6	94.1 94.1	94.1	7.1 7.1	7.1		7.1	5.5 5.4		5.5	7.1		5.5 5.4	5.5	9.2 8.6	8.9
25-Dec-15	Cloudy	Moderate	08:09	3.7	Surface	1.0	20.2 20.2	20.2	8.1 8.1	8.1	27.5 27.7	27.6	93.0 91.3	92.2	7.2 7.0	7.1	7.1	6.2 6.1	6.2	6.2	6.3 5.6	6.0	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	20.2 20.3	20.2	8.1 8.1	8.1	28.3 28.2	28.3	91.6 98.9	95.3	7.0 7.6	7.3		7.3	6.2 6.0		6.1	7.3		6.2 6.0	6.1	5.9 5.3	5.6
28-Dec-15	Sunny	Moderate	09:47	3.7	Surface	1.0	19.4 19.4	19.4	8.1 8.1	8.1	27.9 27.9	27.9	86.2 87.0	86.6	6.7 6.8	6.8	6.8	6.7 6.5	6.6	6.6	10.9 11.3	11.1	10.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	19.4 19.4	19.4	8.1 8.1	8.1	28.0 28.0	28.0	86.9 86.6	86.8	6.8 6.8	6.8		6.8	6.6 6.6		6.6	6.8		6.6 6.6	6.6	10.6 9.6	10.1
30-Dec-15	Cloudy	Moderate	11:33	3.6	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.2 28.2	28.2	90.2 92.1	91.2	7.0 7.2	7.1	7.1	4.9 5.0	5.0	5.0	5.0 6.2	5.6	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	19.3 19.3	19.3	8.2 8.2	8.2	28.2 28.2	28.2	92.6 90.8	91.7	7.2 7.1	7.2		7.2	5.0 5.0		5.0	7.2		5.0 5.0	5.0	5.5 6.2	5.9

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:20	10.6	Surface	1.0	20.5 20.4	20.4	8.2 8.1	8.2	21.4 22.6	22.0	93.5 93.4	93.5	7.3 7.3	7.3	7.3	4.0 4.3	4.2	4.3	4.4 4.3	4.4	4.9
					Middle	5.3	20.4 20.4	20.4	8.1 8.1	8.1	24.7 23.4	24.0	92.2 92.2	92.2	7.3 7.3	7.3		4.3 4.2	4.3		4.6 5.5	5.1	
					Bottom	9.6	20.4 20.4	20.4	8.1 8.1	8.1	25.2 25.3	25.2	92.7 92.3	92.5	7.2 7.2	7.2		4.5 4.3	4.4		5.4 5.0	5.2	
4-Dec-15	Cloudy	Moderate	06:04	10.4	Surface	1.0	19.4 19.4	19.4	8.1 8.1	8.1	29.6 29.5	29.6	96.2 96.8	96.5	7.3 7.3	7.3	7.3	3.4 3.3	3.4	3.6	2.9 2.6	2.8	3.0
					Middle	5.2	19.9 19.9	19.9	8.1 8.1	8.1	30.5 30.2	30.4	93.6 94.4	94.0	7.3 7.3	7.3		3.5 3.6	3.6		3.1 3.5	3.1	
					Bottom	9.4	19.7 20.0	19.8	8.1 8.1	8.1	32.8 32.2	32.5	93.9 94.2	94.1	7.2 7.2	7.2		3.7 3.8	3.8		3.1 3.2	3.2	
7-Dec-15	Cloudy	Moderate	10:32	11.0	Surface	1.0	19.2 19.3	19.3	8.2 8.2	8.2	35.0 35.0	35.0	92.7 92.6	92.7	6.9 7.0	6.9	6.9	3.5 3.5	3.5	3.7	4.4 4.3	4.4	4.7
					Middle	5.5	19.5 19.5	19.5	8.2 8.2	8.2	35.3 35.3	35.3	91.5 91.9	91.7	6.9 6.9	6.9		3.6 3.7	3.7		3.3 5.0	4.2	
					Bottom	10.0	19.5 19.5	19.5	8.2 8.1	8.2	35.3 35.4	35.3	91.2 90.7	91.0	6.8 6.8	6.8		3.8 3.9	3.9		4.8 6.0	5.4	
9-Dec-15	Rainy	Moderate	11:14	11.1	Surface	1.0	18.6 18.6	18.6	8.2 8.2	8.2	35.7 35.7	35.7	100.3 95.4	97.9	7.6 7.2	7.4	7.3	4.3 4.4	4.4	4.6	3.7 2.9	3.3	3.3
					Middle	5.6	18.5 18.5	18.5	8.2 8.2	8.2	35.7 35.7	35.7	93.6 95.9	94.8	7.1 7.3	7.2		4.6 4.6	4.6		2.9 3.4	3.2	
					Bottom	10.1	18.5 18.4	18.5	8.2 8.2	8.2	35.7 35.8	35.8	93.1 95.0	94.1	7.0 7.2	7.1		4.6 4.8	4.7		3.7 3.2	3.5	
11-Dec-15	Sunny	Moderate	12:47	10.6	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	28.1 28.1	28.1	93.9 93.6	93.8	7.4 7.4	7.4	7.4	5.9 5.9	5.9	6.3	5.5 5.0	5.3	5.4
					Middle	5.3	18.2 18.2	18.2	8.2 8.2	8.2	29.3 29.1	29.2	92.6 92.4	92.5	7.3 7.4	7.3		6.4 6.6	6.5		5.4 5.3	5.4	
					Bottom	9.6	18.3 18.3	18.3	8.2 8.2	8.2	29.2 29.2	29.2	92.0 92.6	92.3	7.3 7.3	7.3		6.5 6.5	6.5		5.6 5.6	5.6	
14-Dec-15	Rainy	Moderate	14:39	10.6	Surface	1.0	17.9 17.9	17.9	8.1 8.1	8.1	20.1 20.1	20.1	91.8 92.6	92.2	7.6 7.6	7.6	7.6	6.1 6.1	6.1	6.4	5.3 6.3	5.8	6.1
					Middle	5.3	18.1 18.1	18.1	8.1 8.1	8.1	21.9 20.6	21.3	91.0 92.9	92.0	7.5 7.5	7.5		6.4 6.3	6.4		5.9 6.0	6.0	
					Bottom	9.6	18.0 18.2	18.1	8.1 8.1	8.1	26.6 26.3	26.5	92.0 91.6	91.8	7.4 7.4	7.4		6.6 6.5	6.6		6.0 6.7	6.4	
16-Dec-15	Sunny	Moderate	16:33	10.4	Surface	1.0	17.5 17.6	17.5	8.2 8.2	8.2	26.5 26.6	26.6	92.6 93.3	93.0	7.6 7.5	7.6	7.5	6.3 6.2	6.3	6.4	11.0 11.5	11.3	11.4
					Middle	5.2	17.8 17.8	17.8	8.2 8.2	8.2	27.2 27.2	27.2	91.6 91.3	91.5	7.4 7.4	7.4		6.4 6.6	6.5		11.3 10.8	11.1	
					Bottom	9.4	17.7 17.8	17.8	8.2 8.2	8.2	27.3 27.7	27.5	90.8 90.2	90.5	7.4 7.3	7.3		6.4 6.6	6.5		12.8 11.0	11.9	
18-Dec-15	Sunny	Moderate	12:50	10.3	Surface	1.0	16.7 16.6	16.7	8.1 8.1	8.1	29.8 29.9	29.8	92.9 92.5	92.7	7.6 7.5	7.5	7.6	7.6 7.3	7.5	7.6	7.8 8.2	8.0	8.2
					Middle	5.2	16.6 16.6	16.6	8.1 8.1	8.1	29.9 29.9	29.9	92.4 94.2	93.3	7.5 7.7	7.6		7.8 7.5	7.7		8.4 8.4	8.4	
					Bottom	9.3	16.6 16.6	16.6	8.1 8.1	8.1	29.9 30.0	29.9	94.1 92.2	93.2	7.7 7.5	7.6		7.6 7.6	7.6		7.5 8.7	8.1	
21-Dec-15	Cloudy	Moderate	09:09	10.6	Surface	1.0	15.6 15.7	15.7	8.2 8.1	8.2	32.6 32.7	32.7	96.8 96.5	96.7	7.8 7.8	7.8	7.8	3.8 3.7	3.8	3.9	5.1 3.7	4.4	4.3
					Middle	5.3	16.0 16.0	16.0	8.1 8.1	8.1	33.8 34.6	34.2	96.0 95.7	95.9	7.7 7.7	7.7		3.8 3.9	3.9		3.1 3.3	3.2	
					Bottom	9.6	15.9 16.2	16.0	8.1 8.1	8.1	34.4 35.3	34.8	94.4 95.8	95.1	7.7 7.7	7.7		3.9 3.9	3.9		4.9 5.7	5.3	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	11:01	11.0	Surface	1.0	16.3 16.3	16.3	8.1 8.1	8.1	28.9 28.9	28.9	95.3 94.6	95.0	7.9 7.8	7.8	7.8	4.6 4.8	4.7	4.9	4.5 4.0	4.3	5.6
					Middle	5.5	16.3 16.3	16.3	8.1 8.1	8.1	30.3 31.2	30.7	92.9 94.5	93.7	7.7 7.7	7.7		4.8 5.0	4.9		6.3 5.3	5.8	
					Bottom	10.0	16.3 16.3	16.3	8.1 8.1	8.1	30.9 33.5	32.2	93.0 92.2	92.6	7.6 7.6	7.6		5.1 5.2	5.2		7.3 6.2	6.8	
25-Dec-15	Cloudy	Moderate	12:37	11.1	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	24.6 25.0	24.8	94.4 93.0	93.7	7.9 7.8	7.8	7.8	7.9 7.8	7.9	7.9	7.4 7.4	7.4	8.3
					Middle	5.6	16.7 16.8	16.7	8.1 8.1	8.1	24.9 25.2	25.0	93.2 92.6	92.9	7.8 7.7	7.8		8.0 7.8	7.9		9.1 8.5	8.8	
					Bottom	10.1	16.8 16.7	16.8	8.1 8.1	8.1	25.2 25.1	25.2	92.5 93.2	92.9	7.7 7.8	7.8		7.9 8.0	8.0		9.2 8.3	8.8	
28-Dec-15	Sunny	Moderate	14:35	10.7	Surface	1.0	16.1 16.1	16.1	8.2 8.1	8.2	26.0 26.1	26.1	94.9 95.0	95.0	8.0 8.0	8.0	8.0	5.3 5.2	5.3	5.5	6.5 6.0	6.3	7.2
					Middle	5.4	16.1 16.0	16.1	8.1 8.2	8.1	26.2 26.1	26.1	94.9 94.9	94.9	8.0 8.0	8.0		5.4 5.5	5.5		7.1 8.0	7.6	
					Bottom	9.7	16.1 16.1	16.1	8.1 8.2	8.1	26.3 26.1	26.2	94.9 94.6	94.8	8.0 8.0	8.0		5.7 5.8	5.8		7.8 7.6	7.7	
30-Dec-15	Cloudy	Moderate	16:07	10.5	Surface	1.0	16.0 16.0	16.0	8.2 8.2	8.2	25.7 25.8	25.7	93.2 92.5	92.9	7.9 7.8	7.8	7.8	4.7 4.8	4.8	5.1	4.9 3.1	4.0	3.5
					Middle	5.3	16.1 16.0	16.1	8.2 8.2	8.2	27.3 27.1	27.2	91.9 92.4	92.2	7.7 7.7	7.7		5.2 5.3	5.3		2.9 3.3	3.1	
					Bottom	9.5	16.1 16.1	16.1	8.2 8.2	8.2	27.3 27.2	27.2	94.1 94.9	94.5	7.9 7.9	7.9		5.3 5.1	5.2		3.1 3.4	3.3	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	12:44	10.7	Surface	1.0	20.3 20.3	20.3	8.1 8.1	8.1	29.0 29.0	29.0	92.2 92.6	92.4	7.0 7.1	7.0	7.0	7.5 7.4	7.5	7.7	9.6 8.8	9.2	9.6
					Middle	5.4	20.3 20.3	20.3	8.1 8.1	8.1	29.6 29.2	29.4	91.9 92.1	92.0	7.0 7.0	7.0		7.6 7.7	7.7		9.5 8.3	8.9	
					Bottom	9.7	20.3 20.3	20.3	8.1 8.1	8.1	29.7 29.8	29.8	91.4 91.5	91.5	7.0 7.0	7.0		7.9 7.9	7.9		11.1 10.3	10.7	
4-Dec-15	Cloudy	Moderate	14:58	10.4	Surface	1.0	19.6 19.9	19.7	8.2 8.2	8.2	23.6 24.1	24.1	91.7 91.4	91.6	7.3 7.1	7.2	7.2	4.1 4.2	4.2	4.5	3.7 4.2	4.0	3.9
					Middle	5.2	19.8 20.2	20.0	8.2 8.2	8.2	25.0 25.9	25.4	89.0 90.0	89.5	7.0 7.1	7.1		4.5 4.6	4.6		3.4 3.2	3.3	
					Bottom	9.4	20.3 20.3	20.3	8.1 8.1	8.1	26.6 27.7	27.2	87.9 88.5	88.2	6.8 7.0	6.9		4.7 4.8	4.8		4.1 4.6	4.4	
7-Dec-15	Cloudy	Moderate	16:38	11.2	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	31.1 31.0	31.0	92.8 93.0	92.9	7.1 7.1	7.1	7.1	3.4 3.3	3.4	3.5	6.2 6.0	6.1	6.3
					Middle	5.6	19.4 19.5	19.5	8.2 8.2	8.2	31.3 31.1	31.2	92.5 92.7	92.6	7.1 7.1	7.1		3.5 3.5	3.5		5.3 7.2	6.3	
					Bottom	10.2	19.5 19.4	19.4	8.2 8.2	8.2	31.4 31.2	31.3	91.6 92.3	92.0	7.0 7.1	7.0		3.6 3.6	3.6		6.5 6.4	6.5	
9-Dec-15	Rainy	Moderate	16:46	10.7	Surface	1.0	18.6 18.6	18.6	8.2 8.2	8.2	29.5 29.5	29.5	93.0 92.6	92.8	7.3 7.3	7.3	7.3	6.2 6.4	6.3	6.5	2.9 2.8	2.9	3.9
					Middle	5.4	18.6 18.6	18.6	8.2 8.2	8.2	29.7 29.7	29.7	92.5 93.0	92.8	7.3 7.3	7.3		6.4 6.6	6.5		4.9 3.7	4.3	
					Bottom	9.7	18.6 18.6	18.6	8.2 8.2	8.2	29.6 29.7	29.6	92.5 91.9	92.2	7.3 7.2	7.2		6.4 6.8	6.6		4.3 4.6	4.5	
11-Dec-15	Sunny	Moderate	07:27	10.8	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	32.4 32.0	32.2	98.7 94.7	96.7	7.6 7.4	7.5	7.5	8.9 9.1	9.0	9.7	7.3 8.1	7.7	7.6
					Middle	5.4	18.2 18.2	18.2	8.2 8.2	8.2	32.2 33.1	32.6	94.7 96.7	95.7	7.4 7.5	7.4		10.1 10.0	10.1		7.4 7.5	7.5	
					Bottom	9.8	18.2 18.2	18.2	8.2 8.2	8.2	32.3 34.0	33.2	93.9 95.8	94.9	7.3 7.5	7.4		10.2 10.0	10.1		7.4 7.6	7.5	
14-Dec-15	Rainy	Moderate	09:51	10.8	Surface	1.0	18.0 18.0	18.0	8.1 8.1	8.1	29.5 28.3	28.9	95.7 95.8	95.8	7.5 7.5	7.5	7.5	5.9 5.7	5.8	6.1	6.3 6.3	6.3	6.4
					Middle	5.4	18.1 18.2	18.1	8.1 8.1	8.1	30.7 29.8	30.2	94.0 93.9	94.0	7.4 7.4	7.4		6.0 6.1	6.1		6.5 6.4	6.5	
					Bottom	9.8	18.1 18.2	18.1	8.1 8.1	8.1	30.1 32.1	31.1	92.0 93.7	92.9	7.4 7.4	7.4		6.3 6.4	6.4		5.8 7.2	6.5	
16-Dec-15	Sunny	Moderate	11:08	10.9	Surface	1.0	17.6 17.6	17.6	8.1 8.1	8.1	31.5 30.3	30.9	98.9 94.1	96.5	7.8 7.5	7.6	7.5	11.6 11.6	11.6	11.5	9.3 9.3	9.3	9.9
					Middle	5.5	17.6 17.6	17.6	8.1 8.0	8.1	30.9 32.0	31.4	91.8 95.2	93.5	7.3 7.5	7.4		11.5 11.4	11.5		9.4 10.4	9.9	
					Bottom	9.9	17.6 17.6	17.6	8.1 8.0	8.1	31.0 32.8	31.9	91.4 93.5	92.5	7.3 7.4	7.3		11.5 11.2	11.4		10.2 10.5	10.4	
18-Dec-15	Cloudy	Moderate	05:32	10.6	Surface	1.0	15.8 15.8	15.8	8.1 8.1	8.1	29.2 30.0	29.6	99.0 99.0	99.0	8.2 8.2	8.2	8.3	7.1 7.5	7.3	7.5	6.2 6.5	6.4	6.6
					Middle	5.3	15.9 15.8	15.8	8.1 8.1	8.1	29.4 30.9	30.2	103.2 99.4	101.3	8.5 8.2	8.4		7.3 7.6	7.5		6.2 6.3	6.3	
					Bottom	9.6	15.9 15.8	15.8	8.1 8.1	8.1	29.6 31.5	30.6	104.6 106.1	105.4	8.6 8.7	8.6		7.5 7.7	7.6		6.2 7.8	7.0	
21-Dec-15	Sunny	Moderate	15:18	10.7	Surface	1.0	16.1 16.1	16.1	8.2 8.2	8.2	28.5 28.7	28.6	95.8 95.9	95.9	7.9 7.9	7.9	7.9	4.1 4.3	4.2	5.0	5.2 5.2	5.2	4.3
					Middle	5.4	16.2 16.1	16.2	8.2 8.2	8.2	29.1 29.0	29.0	95.5 95.2	95.4	7.9 7.9	7.9		5.5 5.7	5.6		4.9 4.4	4.7	
					Bottom	9.7	16.3 16.2	16.3	8.2 8.2	8.2	29.6 29.3	29.5	95.9 96.2	96.1	7.9 7.9	7.9		5.3 5.3	5.3		2.6 3.3	3.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	17:12	11.1	Surface	1.0	16.4 16.5	16.4	8.1 8.1	8.1	23.9 23.9	23.9	95.1 95.4	95.3	8.1 8.1	8.1	8.1	4.3 4.4	4.4	4.6	8.4 6.7	7.6	5.6
					Middle	5.6	16.3 16.3	16.3	8.1 8.1	8.1	25.6 24.4	25.0	95.1 94.9	95.0	8.0 8.0	8.0		4.5 4.6	4.6		5.7 5.1	5.4	
					Bottom	10.1	16.3 16.3	16.3	8.1 8.1	8.1	26.1 26.0	26.1	95.1 95.1	95.1	8.0 8.0	8.0		4.7 4.6	4.7		3.7 3.9	3.8	
25-Dec-15	Cloudy	Moderate	07:35	11.1	Surface	1.0	16.7 16.7	16.7	8.1 8.0	8.1	27.5 27.1	27.3	105.3 98.0	101.7	8.7 8.1	8.4	8.3	6.3 6.4	6.4	6.4	6.3 5.3	5.8	6.7
					Middle	5.6	16.7 16.7	16.7	8.0 8.1	8.1	27.4 27.7	27.6	98.0 99.7	98.9	8.1 8.2	8.1		6.4 6.3	6.4		7.1 6.9	7.0	
					Bottom	10.1	16.7 16.7	16.7	8.1 8.0	8.1	27.9 27.7	27.8	97.6 95.0	96.3	8.0 7.9	7.9		6.5 6.5	6.5		7.1 7.2	7.2	
28-Dec-15	Sunny	Moderate	09:48	10.7	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	28.1 29.4	28.8	96.4 96.1	96.3	8.0 8.0	8.0	8.0	10.1 10.1	10.1	10.5	13.4 13.8	13.6	14.2
					Middle	5.4	15.9 15.9	15.9	8.0 8.1	8.1	29.9 28.4	29.1	95.3 95.6	95.5	8.0 8.0	8.0		10.5 10.6	10.6		13.9 14.7	14.3	
					Bottom	9.7	15.9 15.9	15.9	8.0 8.1	8.1	30.3 28.8	29.6	94.9 95.4	95.2	7.8 7.9	7.8		10.9 10.9	10.9		14.4 14.8	14.6	
30-Dec-15	Cloudy	Moderate	10:58	10.6	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	30.9 30.2	30.6	94.3 93.4	93.9	7.7 7.7	7.7	7.8	9.3 8.9	9.1	9.3	10.6 10.0	10.3	10.7
					Middle	5.3	16.0 16.0	16.0	8.1 8.1	8.1	30.5 31.2	30.8	95.0 96.2	95.6	7.8 7.9	7.8		9.4 9.2	9.3		10.0 11.3	10.7	
					Bottom	9.6	16.0 16.0	16.0	8.1 8.1	8.1	30.8 31.9	31.4	95.8 96.6	96.2	7.9 7.9	7.9		9.6 9.4	9.5		10.2 11.9	11.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:29	10.7	Surface	1.0	20.4 20.4	20.4	8.1 8.1	8.1	21.9 22.0	22.0	95.2 95.3	95.3	7.5 7.5	7.5	7.5	4.7 4.7	4.7	4.8	4.9 5.8	5.4	5.1
					Middle	5.4	20.4 20.4	20.4	8.1 8.1	8.1	24.1 23.9	24.0	93.3 94.8	94.1	7.5 7.5	7.5		4.8 4.8	4.8		4.8 4.5	4.7	
					Bottom	9.7	20.4 20.4	20.4	8.1 8.1	8.1	25.3 24.6	24.9	92.5 92.8	92.7	7.3 7.3	7.3		4.8 4.9	4.9		4.7 5.8	5.3	
4-Dec-15	Cloudy	Moderate	05:51	10.3	Surface	1.0	19.3 19.3	19.3	8.1 8.1	8.1	29.6 29.7	29.7	90.0 88.6	89.3	6.7 6.9	6.8	6.7	4.0 3.9	4.0	4.3	3.8 2.4	3.1	3.2
					Middle	5.2	20.5 20.2	20.3	8.1 8.1	8.1	33.1 31.0	32.1	87.1 89.9	88.5	6.6 6.6	6.6		4.3 4.2	4.3		3.3 2.8	3.1	
					Bottom	9.3	20.5 20.5	20.5	8.1 8.1	8.1	33.6 33.6	33.6	88.2 88.4	88.3	6.5 6.6	6.5		4.6 4.5	4.6		2.4 4.2	3.3	
7-Dec-15	Cloudy	Moderate	10:00	10.3	Surface	1.0	19.4 19.4	19.4	8.1 8.2	8.2	35.2 35.2	35.2	93.5 92.9	93.2	7.0 6.9	7.0	7.0	2.7 2.6	2.7	2.8	5.2 5.1	5.2	5.3
					Middle	5.2	19.4 19.4	19.4	8.1 8.2	8.2	35.3 35.3	35.3	92.8 92.9	92.9	6.9 6.9	6.9		2.7 2.7	2.7		5.3 4.7	5.0	
					Bottom	9.3	19.4 19.4	19.4	8.1 8.2	8.1	35.4 35.3	35.3	92.8 92.8	92.8	6.9 6.9	6.9		2.9 2.8	2.9		5.7 5.4	5.6	
9-Dec-15	Rainy	Moderate	11:04	11.1	Surface	1.0	18.8 18.8	18.8	8.2 8.2	8.2	35.8 35.8	35.8	92.0 91.9	92.0	6.9 6.9	6.9	6.9	4.1 4.0	4.1	4.2	8.5 8.7	8.6	8.6
					Middle	5.6	18.7 18.7	18.7	8.2 8.2	8.2	35.8 35.8	35.8	91.4 91.6	91.5	6.9 6.9	6.9		4.1 4.1	4.1		8.6 8.4	8.5	
					Bottom	10.1	18.7 18.7	18.7	8.2 8.2	8.2	35.8 35.8	35.8	91.3 91.5	91.4	6.9 6.9	6.9		4.3 4.4	4.4		9.0 8.3	8.7	
11-Dec-15	Sunny	Moderate	12:58	10.5	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	28.3 28.2	28.2	92.8 92.9	92.9	7.3 7.3	7.3	7.3	6.0 6.0	6.0	6.3	5.0 5.8	5.4	5.7
					Middle	5.3	18.3 18.2	18.3	8.2 8.2	8.2	29.2 29.4	29.3	92.2 92.5	92.4	7.3 7.3	7.3		6.5 6.6	6.6		5.6 4.7	5.2	
					Bottom	9.5	18.3 18.3	18.3	8.2 8.2	8.2	29.2 29.4	29.3	91.9 92.1	92.0	7.3 7.3	7.3		6.4 6.4	6.4		6.5 6.2	6.4	
14-Dec-15	Rainy	Moderate	14:49	10.7	Surface	1.0	17.9 17.9	17.9	8.1 8.1	8.1	20.8 20.0	20.4	93.3 92.8	93.1	7.7 7.7	7.7	7.7	5.3 5.3	5.3	5.5	6.6 6.0	6.3	6.4
					Middle	5.4	18.0 18.0	18.0	8.1 8.1	8.1	21.6 22.0	21.8	92.2 94.0	93.1	7.7 7.7	7.7		5.5 5.5	5.5		6.3 5.9	6.1	
					Bottom	9.7	18.0 18.1	18.1	8.1 8.1	8.1	24.9 24.8	24.8	94.8 92.2	93.5	7.6 7.6	7.6		5.6 5.7	5.7		7.0 6.3	6.7	
16-Dec-15	Sunny	Moderate	16:47	10.6	Surface	1.0	17.7 17.5	17.6	8.2 8.2	8.2	29.3 26.4	27.8	103.5 92.9	98.2	8.2 7.5	7.9	7.8	6.1 6.1	6.1	6.0	8.7 8.6	8.7	8.7
					Middle	5.3	17.7 17.8	17.7	8.2 8.2	8.2	26.9 30.0	28.4	92.1 97.9	95.0	7.5 7.8	7.6		5.9 5.9	5.9		8.4 7.3	7.9	
					Bottom	9.6	17.8 17.8	17.8	8.2 8.2	8.2	27.0 31.0	29.0	90.8 94.6	92.7	7.4 7.6	7.5		5.9 5.9	5.9		9.6 9.5	9.6	
18-Dec-15	Sunny	Moderate	12:58	10.7	Surface	1.0	16.6 16.7	16.6	8.1 8.1	8.1	30.4 29.5	29.9	97.8 97.2	97.5	7.9 7.9	7.9	8.0	6.6 6.2	6.4	7.8	6.9 6.6	6.8	7.0
					Middle	5.4	16.6 16.6	16.6	8.1 8.1	8.1	30.1 31.5	30.8	100.8 98.2	99.5	8.2 8.0	8.1		8.5 8.3	8.4		7.4 7.7	7.6	
					Bottom	9.7	16.6 16.6	16.6	8.1 8.1	8.1	32.1 30.3	31.2	107.7 104.1	105.9	8.6 8.4	8.5		8.8 8.3	8.6		6.3 6.6	6.5	
21-Dec-15	Cloudy	Moderate	08:57	10.6	Surface	1.0	16.4 16.4	16.4	8.1 8.1	8.1	35.5 35.7	35.6	93.7 94.0	93.9	7.4 7.4	7.4	7.4	4.1 4.3	4.2	4.4	4.8 6.4	5.6	5.0
					Middle	5.3	16.4 16.4	16.4	8.1 8.1	8.1	35.8 35.6	35.7	93.8 93.7	93.8	7.4 7.4	7.4		4.4 4.5	4.5		4.2 5.0	4.6	
					Bottom	9.6	16.4 16.4	16.4	8.1 8.1	8.1	35.7 35.8	35.7	93.4 93.7	93.6	7.4 7.4	7.4		4.5 4.5	4.5		5.0 4.8	4.9	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	10:48	11.1	Surface	1.0	16.3 16.3	16.3	8.1 8.1	8.1	30.6 28.9	29.8	94.6 94.9	94.8	7.7 7.8	7.8	7.8	3.2 3.2	3.2	3.3	5.5 4.3	4.9	5.0
					Middle	5.6	16.3 16.3	16.3	8.1 8.1	8.1	32.7 30.4	31.6	96.0 94.8	95.4	7.6 7.7	7.7		3.4 3.3	3.4		5.4 4.4	4.9	
					Bottom	10.1	16.3 16.4	16.4	8.1 8.1	8.1	33.5 34.6	34.0	95.7 93.7	94.7	7.7 7.5	7.6		3.3 3.4	3.4		4.6 5.5	5.1	
25-Dec-15	Cloudy	Moderate	12:46	11.0	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	24.5 24.3	24.4	95.5 95.5	95.5	8.0 8.0	8.0	7.9	6.3 6.6	6.5	6.6	7.4 8.3	7.9	7.6
					Middle	5.5	16.7 16.7	16.7	8.1 8.1	8.1	24.4 25.0	24.7	93.5 93.3	93.4	7.9 7.8	7.8		6.7 6.4	6.6		7.7 7.3	7.5	
					Bottom	10.0	16.7 16.7	16.7	8.1 8.1	8.1	24.6 25.9	25.3	93.4 93.1	93.3	7.8 7.8	7.8		6.7 6.6	6.7		7.6 7.0	7.3	
28-Dec-15	Sunny	Moderate	14:45	10.7	Surface	1.0	16.0 16.0	16.0	8.2 8.2	8.2	25.6 25.7	25.7	95.6 95.3	95.5	8.1 8.0	8.1	8.1	5.9 5.6	5.8	6.1	7.3 7.7	7.5	7.3
					Middle	5.4	16.0 16.0	16.0	8.2 8.2	8.2	25.6 25.8	25.7	95.2 94.9	95.1	8.0 8.0	8.0		6.1 6.3	6.2		7.1 6.8	7.0	
					Bottom	9.7	16.0 16.0	16.0	8.1 8.2	8.2	25.9 25.7	25.8	94.9 94.6	94.8	8.0 8.0	8.0		6.3 6.2	6.3		6.7 7.9	7.3	
30-Dec-15	Cloudy	Moderate	16:16	10.4	Surface	1.0	16.1 16.0	16.1	8.2 8.2	8.2	27.1 26.8	26.9	97.7 96.1	96.9	8.2 8.1	8.1	8.1	4.6 4.7	4.7	4.8	4.7 4.8	4.8	4.6
					Middle	5.2	16.0 16.0	16.0	8.2 8.2	8.2	27.1 27.7	27.4	96.2 98.8	97.5	8.0 8.2	8.1		4.7 4.8	4.8		4.9 5.2	5.1	
					Bottom	9.4	16.1 16.1	16.1	8.2 8.2	8.2	27.2 28.4	27.8	96.8 100.9	98.9	8.1 8.4	8.2		4.7 4.8	4.8		4.1 3.8	4.0	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	12:35	10.7	Surface	1.0	20.3 20.4	20.3	8.1 8.1	8.1	28.5 28.8	28.6	92.3 92.3	92.3	7.0 7.0	7.0	7.0	6.1 5.9	6.0	6.1	6.1 4.9	5.5	6.1
					Middle	5.4	20.2 20.2	20.2	8.1 8.1	8.1	29.5 29.5	29.5	91.1 92.0	91.6	6.9 7.0	7.0		6.1 6.1	6.1		5.9 6.8	6.4	
					Bottom	9.7	20.3 20.2	20.3	8.1 8.1	8.1	29.6 29.7	29.6	90.6 90.5	90.6	6.9 6.9	6.9		6.3 6.2	6.3		6.5 6.2	6.4	
4-Dec-15	Cloudy	Moderate	15:12	10.3	Surface	1.0	19.8 19.6	19.7	8.2 8.2	8.2	22.5 24.0	23.2	91.1 91.8	91.5	7.1 7.1	7.1	7.1	4.4 4.4	4.4	4.6	4.4 5.1	4.8	5.4
					Middle	5.2	20.2 20.1	20.1	8.2 8.2	8.2	25.4 25.6	25.5	89.7 90.2	90.0	7.1 7.0	7.1		4.5 4.6	4.6		4.8 5.4	5.1	
					Bottom	9.3	20.1 20.2	20.1	8.2 8.2	8.2	26.1 26.3	26.2	89.8 89.4	89.6	7.0 7.0	7.0		4.8 4.9	4.9		6.3 6.2	6.3	
7-Dec-15	Cloudy	Moderate	16:50	10.4	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	30.6 30.3	30.5	94.6 95.1	94.9	7.3 7.3	7.3	7.3	4.0 4.1	4.1	4.2	6.3 6.3	6.3	7.9
					Middle	5.2	19.4 19.4	19.4	8.2 8.2	8.2	30.4 31.0	30.7	94.2 93.8	94.0	7.2 7.2	7.2		4.2 4.1	4.2		9.1 8.5	8.8	
					Bottom	9.4	19.4 19.4	19.4	8.2 8.2	8.2	31.5 30.4	31.0	92.9 93.4	93.2	7.1 7.2	7.2		4.3 4.4	4.4		8.0 9.4	8.7	
9-Dec-15	Rainy	Moderate	17:00	11.1	Surface	1.0	18.8 18.8	18.8	8.2 8.2	8.2	30.0 30.2	30.1	95.7 100.7	98.2	7.5 7.8	7.6	7.6	5.2 5.2	5.2	5.3	6.4 6.1	6.3	6.2
					Middle	5.6	18.8 18.8	18.8	8.2 8.2	8.2	30.1 30.3	30.2	95.2 97.0	96.1	7.4 7.5	7.5		5.2 5.4	5.3		6.7 6.5	6.6	
					Bottom	10.1	18.8 18.7	18.8	8.2 8.2	8.2	30.5 30.1	30.3	95.6 92.5	94.1	7.4 7.2	7.3		5.5 5.4	5.5		6.3 5.0	5.7	
11-Dec-15	Sunny	Moderate	07:17	10.2	Surface	1.0	18.3 18.3	18.3	8.2 8.2	8.2	33.7 34.4	34.0	93.7 94.0	93.9	7.2 7.2	7.2	7.2	10.4 10.2	10.3	10.5	12.4 12.8	12.6	12.6
					Middle	5.1	18.2 18.3	18.3	8.2 8.2	8.2	34.8 33.9	34.3	94.0 93.4	93.7	7.2 7.2	7.2		10.5 10.6	10.6		13.0 12.0	12.5	
					Bottom	9.2	18.2 18.3	18.3	8.1 8.2	8.2	35.1 34.1	34.6	92.4 92.6	92.5	7.1 7.1	7.1		10.6 10.8	10.7		12.3 12.8	12.6	
14-Dec-15	Rainy	Moderate	09:41	10.8	Surface	1.0	18.2 18.2	18.2	8.1 8.1	8.1	32.6 32.8	32.7	95.1 94.2	94.7	7.3 7.3	7.3	7.3	7.7 7.6	7.7	8.1	8.3 7.1	7.7	6.9
					Middle	5.4	18.2 18.2	18.2	8.1 8.1	8.1	32.9 32.7	32.8	93.0 94.1	93.6	7.2 7.3	7.3		8.2 8.1	8.2		6.9 6.0	6.5	
					Bottom	9.8	18.2 18.2	18.2	8.1 8.1	8.1	33.9 32.8	33.4	93.0 93.0	93.0	7.2 7.2	7.2		8.5 8.4	8.5		6.7 6.5	6.6	
16-Dec-15	Sunny	Moderate	11:00	10.6	Surface	1.0	17.6 17.6	17.6	8.1 8.1	8.1	32.4 32.8	32.6	93.2 95.6	94.4	7.3 7.5	7.4	7.4	18.4 18.5	18.5	18.4	20.2 19.8	20.0	20.1
					Middle	5.3	17.6 17.6	17.6	8.0 8.1	8.1	32.9 32.6	32.8	94.0 91.8	92.9	7.4 7.2	7.3		18.4 18.2	18.3		19.9 18.6	19.3	
					Bottom	9.6	17.6 17.6	17.6	8.1 8.0	8.0	32.8 32.9	32.9	91.5 92.3	91.9	7.2 7.2	7.2		18.6 18.1	18.4		19.8 22.2	21.0	
18-Dec-15	Cloudy	Moderate	05:22	10.5	Surface	1.0	15.7 15.7	15.7	8.1 8.1	8.1	28.3 28.3	28.3	98.4 97.7	98.1	8.2 8.2	8.2	8.2	6.8 6.6	6.7	6.9	5.9 6.6	6.3	6.4
					Middle	5.3	15.8 15.9	15.9	8.1 8.1	8.1	28.8 28.7	28.8	96.1 98.5	97.3	8.0 8.2	8.1		6.9 7.0	7.0		6.2 6.8	6.5	
					Bottom	9.5	15.8 15.9	15.9	8.1 8.1	8.1	29.5 28.8	29.1	96.9 99.0	98.0	8.0 8.2	8.1		7.1 6.9	7.0		6.1 6.4	6.3	
21-Dec-15	Sunny	Moderate	15:24	10.7	Surface	1.0	16.4 16.4	16.4	8.2 8.2	8.2	29.5 28.8	29.1	97.3 95.3	96.3	8.0 7.8	7.9	7.9	5.5 5.4	5.5	5.6	6.8 6.0	6.4	6.7
					Middle	5.4	16.4 16.4	16.4	8.2 8.2	8.2	29.1 30.1	29.6	95.4 98.5	97.0	7.8 8.0	7.9		5.8 5.5	5.7		4.9 5.6	5.3	
					Bottom	9.7	16.4 16.4	16.4	8.2 8.2	8.2	30.8 29.2	30.0	99.7 96.2	98.0	8.1 7.9	8.0		5.6 5.7	5.7		8.9 7.8	8.4	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	17:27	11.2	Surface	1.0	16.4 16.5	16.4	8.1 8.1	8.1	25.9 25.1	25.5	95.9 96.4	96.2	8.0 8.1	8.1	8.1	5.7 5.8	5.8	6.2	6.6 6.1	6.4	5.9
					Middle	5.6	16.5 16.5	16.5	8.1 8.1	8.1	26.4 26.2	26.3	96.3 95.9	96.1	8.0 8.0	8.0		6.3 6.1	6.2		6.3 4.4	5.4	
					Bottom	10.2	16.5 16.5	16.5	8.1 8.1	8.1	26.3 27.0	26.6	96.1 96.7	96.4	8.0 8.0	8.0		6.4 6.6	6.5		6.6 5.0	5.8	
25-Dec-15	Cloudy	Moderate	07:28	11.3	Surface	1.0	16.7 16.7	16.7	8.0 8.0	8.0	29.9 30.5	30.2	95.7 96.8	96.3	7.7 7.8	7.8	7.8	8.2 8.2	8.2	8.3	8.6 8.6	8.6	9.1
					Middle	5.7	16.8 16.8	16.8	8.0 8.0	8.0	30.6 31.5	31.0	95.2 95.9	95.6	7.7 7.7	7.7		8.3 8.4	8.4		8.4 8.7	8.6	
					Bottom	10.3	16.8 16.8	16.8	8.0 8.0	8.0	31.8 30.7	31.3	93.8 95.1	94.5	7.5 7.7	7.6		8.4 8.4	8.4		10.1 10.1	10.1	
28-Dec-15	Sunny	Moderate	09:38	10.9	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	30.4 29.7	30.0	95.5 95.5	95.5	7.9 7.9	7.9	7.9	20.7 20.6	20.7	20.9	25.8 25.7	25.8	24.9
					Middle	5.5	15.9 15.9	15.9	8.1 8.1	8.1	30.0 30.3	30.2	95.3 95.4	95.4	7.9 7.9	7.9		20.8 20.9	20.9		24.7 25.4	25.1	
					Bottom	9.9	15.9 15.9	15.9	8.1 8.1	8.1	30.9 30.2	30.6	95.4 95.3	95.4	7.8 7.9	7.8		21.1 21.3	21.2		23.8 23.6	23.7	
30-Dec-15	Cloudy	Moderate	10:49	10.8	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	32.5 31.6	32.1	96.5 95.4	96.0	7.8 7.8	7.8	7.8	7.3 7.0	7.2	7.5	8.0 9.8	8.9	7.3
					Middle	5.4	16.0 16.0	16.0	8.1 8.1	8.1	32.6 32.0	32.3	96.6 96.2	96.4	7.8 7.8	7.8		7.7 7.5	7.6		7.4 6.6	7.0	
					Bottom	9.8	16.0 16.0	16.0	8.1 8.1	8.1	32.3 32.7	32.5	96.3 97.0	96.7	7.8 7.9	7.8		7.9 7.6	7.8		6.4 5.8	6.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:36	6.3	Surface	1.0	23.8 23.8	23.8	8.1 8.1	8.1	27.7 27.7	27.7	89.4 90.9	90.2	6.5 6.6	6.5	6.5	6.6 6.7	6.7	6.8	9.6 10.2	9.9	10.2
					Middle	3.2	23.8 23.8	23.8	8.1 8.1	8.1	27.9 27.8	27.8	90.9 90.3	90.6	6.6 6.5	6.5		6.8 6.9	6.9		10.7 10.2	10.5	
					Bottom	5.3	23.8 23.8	23.8	8.1 8.1	8.1	28.4 28.9	28.6	93.1 89.2	91.2	6.7 6.4	6.5		6.8 6.8	6.8		10.3 10.3	10.3	
4-Dec-15	Cloudy	Moderate	06:37	6.3	Surface	1.0	22.8 22.8	22.8	8.1 8.1	8.1	25.1 25.0	25.1	84.5 88.2	86.4	6.3 6.4	6.4	6.4	3.6 3.6	3.6	3.8	4.1 3.6	3.9	3.7
					Middle	3.2	23.5 23.7	23.6	8.1 8.1	8.1	28.3 28.4	28.3	87.7 87.2	87.5	6.3 6.3	6.3		3.8 3.9	3.9		4.2 3.3	3.8	
					Bottom	5.3	23.9 23.1	23.5	8.1 8.1	8.1	29.2 29.8	29.5	86.2 86.9	86.6	6.2 6.3	6.2		3.8 3.8	3.8		3.1 3.5	3.3	
7-Dec-15	Cloudy	Moderate	10:27	6.1	Surface	1.0	22.7 22.8	22.8	8.2 8.2	8.2	30.1 30.2	30.1	86.4 91.9	89.2	6.2 6.6	6.4	6.4	5.7 5.7	5.7	5.9	4.3 4.3	4.3	5.3
					Middle	3.1	23.0 23.0	23.0	8.2 8.2	8.2	30.5 30.5	30.5	85.4 91.3	88.4	6.2 6.6	6.4		5.8 5.9	5.9		5.9 5.7	5.8	
					Bottom	5.1	22.9 23.0	23.0	8.2 8.2	8.2	31.0 30.7	30.9	84.6 90.6	87.6	6.1 6.6	6.3		5.9 6.1	6.0		6.2 5.2	5.7	
9-Dec-15	Rainy	Moderate	11:59	6.1	Surface	1.0	22.0 22.0	22.0	8.2 8.2	8.2	30.8 30.8	30.8	88.7 87.2	88.0	6.5 6.4	6.4	6.5	4.1 3.9	4.0	4.2	3.7 5.3	4.5	4.7
					Middle	3.1	22.0 22.0	22.0	8.2 8.2	8.2	30.9 30.9	30.9	88.8 88.2	88.5	6.5 6.4	6.5		4.3 4.1	4.2		5.1 4.2	4.7	
					Bottom	5.1	22.0 22.0	22.0	8.2 8.2	8.2	30.9 30.9	30.9	88.2 91.3	89.8	6.5 6.7	6.6		4.3 4.3	4.3		4.3 5.2	4.8	
11-Dec-15	Sunny	Moderate	12:39	6.4	Surface	1.0	21.7 21.8	21.8	8.2 8.2	8.2	31.0 31.0	31.0	87.3 87.1	87.2	6.4 6.4	6.4	6.4	11.1 10.5	10.8	11.5	8.9 9.2	9.1	9.5
					Middle	3.2	21.7 21.7	21.7	8.2 8.2	8.2	31.0 31.0	31.0	87.4 86.1	86.8	6.4 6.3	6.4		12.3 11.4	11.9		9.8 9.0	9.4	
					Bottom	5.4	21.7 21.7	21.7	8.2 8.2	8.2	31.0 31.0	31.0	88.8 86.8	87.8	6.5 6.4	6.4		12.5 11.3	11.9		9.9 9.9	9.9	
14-Dec-15	Rainy	Moderate	14:43	6.2	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	28.6 28.6	28.6	92.0 90.5	91.3	6.8 6.8	6.8	6.8	4.3 4.5	4.4	6.5	5.1 4.5	4.8	4.3
					Middle	3.1	21.6 21.6	21.6	8.2 8.2	8.2	29.1 28.8	28.9	89.5 89.5	89.5	6.7 6.7	6.7		7.7 7.6	7.7		3.7 4.6	4.2	
					Bottom	5.2	21.6 21.6	21.6	8.1 8.1	8.1	29.4 29.5	29.4	88.1 89.2	88.7	6.5 6.7	6.6		7.5 7.5	7.5		3.6 4.1	3.9	
16-Dec-15	Sunny	Moderate	16:23	6.3	Surface	1.0	21.1 21.2	21.1	8.2 8.1	8.1	28.2 28.0	28.1	86.8 91.8	89.3	6.6 6.9	6.7	6.8	5.0 4.8	4.9	4.6	8.2 8.1	8.2	9.1
					Middle	3.2	21.3 21.3	21.3	8.1 8.1	8.1	28.5 28.7	28.6	94.8 88.4	91.6	7.1 6.6	6.9		4.3 4.4	4.4		7.6 7.0	7.3	
					Bottom	5.3	21.3 21.3	21.3	8.1 8.1	8.1	28.9 28.8	28.8	91.7 90.1	90.9	6.9 6.8	6.8		4.4 4.8	4.6		11.7 12.0	11.9	
18-Dec-15	Sunny	Moderate	12:27	6.3	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.2 29.3	29.3	92.8 89.5	91.2	7.0 6.8	6.9	6.9	5.5 5.6	5.6	5.6	3.3 5.1	4.2	3.9
					Middle	3.2	20.0 20.1	20.1	8.2 8.2	8.2	30.0 30.1	30.1	91.1 88.3	89.7	6.9 6.7	6.8		5.5 5.6	5.6		3.9 4.0	4.0	
					Bottom	5.3	20.2 20.0	20.1	8.2 8.2	8.2	30.2 30.4	30.3	89.8 87.6	88.7	6.9 6.7	6.8		5.5 5.7	5.6		3.5 3.4	3.5	
21-Dec-15	Cloudy	Moderate	15:14	6.6	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.8 29.8	29.8	88.5 90.0	89.3	6.8 6.9	6.8	6.9	2.7 2.7	2.7	3.0	7.2 7.9	7.6	5.0
					Middle	3.3	19.7 19.7	19.7	8.2 8.2	8.2	30.1 30.2	30.1	88.8 90.3	89.6	6.8 6.9	6.9		3.1 3.0	3.1		3.7 5.1	4.4	
					Bottom	5.6	19.7 19.7	19.7	8.2 8.2	8.2	30.3 30.2	30.3	92.6 88.9	90.8	7.1 6.8	6.9		3.3 3.0	3.2		2.3 3.5	2.9	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	11:17	6.1	Surface	1.0	19.8 19.8	19.8	8.2 8.2	8.2	29.9 29.9	29.9	91.3 90.9	91.1	7.0 7.0	7.0	7.0	3.6 3.5	3.6	3.7	3.7 4.8	4.3	4.1
					Middle	3.1	19.8 19.8	19.8	8.2 8.2	8.2	30.0 30.1	30.1	91.3 89.6	90.5	7.0 6.9	6.9		3.7 3.8	3.8		4.1 3.7	3.9	
					Bottom	5.1	19.8 19.8	19.8	8.2 8.1	8.2	30.1 30.2	30.2	91.8 90.5	91.2	7.0 6.9	7.0		3.8 3.8	3.8		4.1 4.3	4.2	
25-Dec-15	Cloudy	Moderate	12:35	6.1	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	27.2 27.2	27.2	89.4 90.1	89.8	6.9 7.0	6.9	6.9	7.4 7.3	7.4	7.5	6.0 5.9	6.0	6.4
					Middle	3.1	20.3 20.3	20.3	8.1 8.1	8.1	27.9 28.3	28.1	89.7 90.6	90.2	6.9 6.9	6.9		7.5 7.5	7.5		6.8 6.8	6.8	
					Bottom	5.1	20.2 20.4	20.3	8.1 8.1	8.1	28.6 28.7	28.7	89.8 90.0	89.9	6.9 6.9	6.9		7.5 7.6	7.6		6.0 6.7	6.4	
28-Dec-15	Sunny	Moderate	14:27	6.4	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	28.2 28.2	28.2	88.5 90.0	89.3	6.9 7.0	6.9	6.9	6.3 6.3	6.3	6.4	7.2 7.6	7.4	7.2
					Middle	3.2	19.5 19.5	19.5	8.2 8.1	8.2	28.3 28.3	28.3	88.2 90.0	89.1	6.8 7.0	6.9		6.4 6.4	6.4		8.3 6.4	7.4	
					Bottom	5.4	19.6 19.5	19.6	8.1 8.2	8.1	28.4 28.5	28.5	92.5 88.8	90.7	7.2 6.9	7.0		6.5 6.2	6.4		6.9 6.5	6.7	
30-Dec-15	Cloudy	Moderate	15:45	6.2	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	29.0 29.0	29.0	89.7 89.1	89.4	6.9 6.9	6.9	7.0	7.4 7.4	7.4	7.0	10.9 10.3	10.6	10.6
					Middle	3.1	19.5 19.5	19.5	8.2 8.2	8.2	29.0 29.1	29.1	91.3 91.5	91.4	7.1 7.1	7.1		7.6 7.0	7.3		10.1 10.6	10.4	
					Bottom	5.2	19.5 19.6	19.6	8.2 8.2	8.2	29.1 29.2	29.2	91.4 90.8	91.1	7.1 7.0	7.0		6.1 6.6	6.4		10.8 10.9	10.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	12:22	6.2	Surface	1.0	23.6 23.5	23.6	8.1 8.1	8.1	25.3 25.5	25.4	88.6 88.3	88.5	6.5 6.5	6.5	6.6	8.1 8.4	8.3	8.6	2.3 3.9	3.1	3.2
					Middle	3.1	23.6 23.5	23.6	8.1 8.1	8.1	25.6 25.6	25.6	90.5 88.7	89.6	6.6 6.5	6.6		8.6 8.8	8.7		4.1 3.1	3.6	
					Bottom	5.2	23.6 23.6	23.6	8.1 8.1	8.1	25.9 25.5	25.7	87.2 89.5	88.4	6.4 6.6	6.5		8.7 8.8	8.8		2.3 3.4	2.9	
4-Dec-15	Cloudy	Moderate	13:57	6.3	Surface	1.0	22.9 22.9	22.9	8.1 8.1	8.1	27.2 27.2	27.2	87.9 89.0	88.5	6.5 6.5	6.5	6.5	2.9 2.9	2.9	3.2	2.4 3.3	2.9	3.1
					Middle	3.2	23.2 23.1	23.1	8.1 8.1	8.1	27.1 27.3	27.2	86.8 86.8	86.8	6.4 6.4	6.4		3.4 3.2	3.3		3.2 3.8	3.5	
					Bottom	5.3	23.4 23.2	23.3	8.1 8.1	8.1	28.7 29.9	29.3	89.2 88.2	88.7	6.4 6.4	6.4		3.4 3.5	3.5		2.6 2.9	2.8	
7-Dec-15	Cloudy	Moderate	16:02	6.4	Surface	1.0	22.6 22.5	22.5	8.2 8.2	8.2	30.0 30.2	30.1	89.6 85.2	87.4	6.5 6.2	6.4	6.4	7.4 7.3	7.4	7.5	8.5 8.1	8.3	8.4
					Middle	3.2	22.8 22.8	22.8	8.2 8.2	8.2	31.2 31.1	31.2	87.1 91.5	89.3	6.3 6.6	6.4		7.6 7.6	7.6		9.0 7.8	8.4	
					Bottom	5.4	22.8 22.7	22.8	8.2 8.2	8.2	31.3 31.4	31.3	94.0 87.7	90.9	6.8 6.3	6.5		7.5 7.6	7.6		8.2 8.8	8.5	
9-Dec-15	Rainy	Moderate	16:48	6.5	Surface	1.0	22.0 22.0	22.0	8.2 8.2	8.2	30.7 30.7	30.7	87.6 92.9	90.3	6.4 6.8	6.6	6.6	7.7 7.8	7.8	7.9	7.9 7.5	7.7	7.6
					Middle	3.3	22.0 22.0	22.0	8.2 8.2	8.2	30.7 30.7	30.7	88.6 92.7	90.7	6.5 6.8	6.6		7.8 7.9	7.9		7.9 7.3	7.6	
					Bottom	5.5	22.0 22.0	22.0	8.2 8.2	8.2	30.6 30.7	30.7	92.8 88.9	90.9	6.8 6.5	6.7		8.0 7.9	8.0		8.0 7.2	7.6	
11-Dec-15	Sunny	Moderate	07:27	6.3	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.8	30.8	87.1 86.9	87.0	6.4 6.4	6.4	6.4	10.8 11.4	11.1	11.1	9.9 10.0	10.0	9.8
					Middle	3.2	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.8	30.8	87.1 87.0	87.1	6.4 6.4	6.4		11.5 11.0	11.3		9.9 10.1	10.0	
					Bottom	5.3	21.6 21.6	21.6	8.2 8.2	8.2	30.8 30.7	30.8	87.0 87.0	87.0	6.4 6.4	6.4		11.3 10.7	11.0		9.4 9.1	9.3	
14-Dec-15	Rainy	Moderate	09:56	6.2	Surface	1.0	21.5 21.6	21.5	8.1 8.1	8.1	28.4 28.5	28.4	88.6 91.9	90.3	6.6 6.9	6.7	6.8	5.5 5.8	5.7	7.0	6.4 5.9	6.2	7.0
					Middle	3.1	21.6 21.6	21.6	8.1 8.1	8.1	28.6 29.0	28.6	90.1 93.5	91.8	6.7 7.0	6.8		7.6 7.5	7.6		6.8 7.1	7.0	
					Bottom	5.2	21.6 21.6	21.6	8.1 8.1	8.1	28.7 29.2	29.1	88.3 91.2	89.8	6.6 6.8	6.7		7.8 7.5	7.7		8.6 7.1	7.9	
16-Dec-15	Sunny	Moderate	11:16	6.3	Surface	1.0	20.8 20.8	20.8	8.2 8.2	8.2	28.1 28.1	28.1	89.4 87.6	88.5	6.8 6.7	6.7	6.7	5.6 5.2	5.4	6.0	5.9 5.9	5.9	6.2
					Middle	3.2	21.1 20.9	21.0	8.2 8.2	8.2	28.3 28.2	28.2	87.4 87.0	87.2	6.6 6.6	6.6		6.6 6.0	6.3		6.5 5.1	5.8	
					Bottom	5.3	21.0 21.2	21.1	8.2 8.1	8.2	28.5 28.5	28.5	86.7 85.5	86.1	6.5 6.4	6.5		6.1 6.5	6.3		6.7 6.9	6.8	
18-Dec-15	Cloudy	Moderate	05:33	6.3	Surface	1.0	19.4 19.6	19.5	8.2 8.2	8.2	29.1 28.8	29.0	88.4 89.3	88.9	6.7 6.8	6.8	6.8	5.2 5.3	5.3	5.4	3.8 3.6	3.7	3.9
					Middle	3.2	20.0 19.8	19.9	8.2 8.2	8.2	29.8 29.8	29.8	87.9 87.9	87.9	6.7 6.8	6.8		5.5 5.3	5.4		4.2 4.3	4.3	
					Bottom	5.3	20.1 19.9	20.0	8.2 8.2	8.2	30.0 30.1	30.1	87.5 87.0	87.3	6.7 6.7	6.7		5.3 5.5	5.4		4.1 3.0	3.6	
21-Dec-15	Sunny	Moderate	09:12	6.4	Surface	1.0	19.9 20.0	20.0	8.2 8.2	8.2	30.8 30.8	30.8	85.8 84.9	85.4	6.5 6.4	6.5	6.5	2.9 2.9	2.9	2.9	6.6 5.0	5.8	4.9
					Middle	3.2	20.0 20.1	20.1	8.2 8.2	8.2	30.8 30.9	30.9	85.2 84.4	84.8	6.5 6.4	6.4		2.9 2.9	2.9		5.0 3.8	4.4	
					Bottom	5.4	20.2 20.1	20.1	8.2 8.2	8.2	31.0 31.0	31.0	84.5 85.5	85.0	6.4 6.5	6.4		2.9 3.0	3.0		4.7 4.5	4.6	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	16:35	6.2	Surface	1.0	20.0 20.0	20.0	8.2 8.2	8.2	28.4 28.4	28.4	89.7 90.0	89.9	6.9 6.9	6.9	6.9	5.5 5.5	5.5	5.4	4.2 5.2	4.7	4.8
					Middle	3.1	20.1 20.1	20.1	8.2 8.2	8.2	30.0 30.0	30.0	89.7 90.2	90.0	6.8 6.8	6.8		5.3 5.3	5.3		2.8 4.5	3.7	
					Bottom	5.2	20.1 20.1	20.1	8.2 8.2	8.2	30.2 30.3	30.2	90.2 90.9	90.6	6.9 6.9	6.9		5.2 5.4	5.3		6.8 5.3	6.1	
25-Dec-15	Cloudy	Moderate	07:48	6.1	Surface	1.0	20.1 20.1	20.1	8.1 8.1	8.1	26.9 26.9	26.9	91.0 92.4	91.7	7.1 7.2	7.1	7.1	8.1 8.2	8.2	8.3	7.0 8.5	7.8	7.8
					Middle	3.1	20.1 20.1	20.1	8.1 8.1	8.1	27.1 27.0	27.1	90.4 93.8	92.1	7.0 7.3	7.1		8.2 8.3	8.3		7.4 8.2	7.8	
					Bottom	5.1	20.1 20.1	20.1	8.1 8.1	8.1	27.2 27.1	27.1	89.0 94.8	91.9	6.9 7.3	7.1		8.4 8.3	8.4		7.6 7.8	7.7	
28-Dec-15	Sunny	Moderate	09:25	6.2	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	91.9 88.2	90.1	7.2 6.9	7.0	7.0	9.3 8.9	9.1	9.6	8.1 8.2	8.2	10.3
					Middle	3.1	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	88.1 92.1	90.1	6.9 7.2	7.0		9.6 10.4	10.0		11.7 11.7	11.7	
					Bottom	5.2	19.5 19.4	19.4	8.2 8.2	8.2	28.0 28.1	28.0	95.2 88.7	92.0	7.4 6.9	7.2		10.0 9.3	9.7		11.2 10.7	11.0	
30-Dec-15	Cloudy	Moderate	10:59	6.4	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	28.6 28.6	28.6	85.9 86.7	86.3	6.7 6.7	6.7	6.7	3.9 4.0	4.0	5.0	4.0 3.8	3.9	4.1
					Middle	3.2	19.6 19.6	19.6	8.2 8.2	8.2	28.8 28.9	28.8	85.6 86.0	85.8	6.6 6.6	6.6		4.8 5.1	5.0		4.6 3.9	4.3	
					Bottom	5.4	19.7 19.7	19.7	8.1 8.1	8.1	29.3 29.2	29.2	85.5 86.7	86.1	6.6 6.7	6.6		6.4 5.8	6.1		3.3 5.1	4.2	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	16:49	8.1	Surface	1.0	23.8 23.8	23.8	8.0 8.0	8.0	27.1 27.0	27.0	87.3 86.9	87.1	6.3 6.3	6.3	6.3	10.1 10.6	10.4	10.5	7.0 7.4	7.2	8.2
					Middle	4.1	23.7 23.7	23.7	8.0 8.0	8.0	27.0 27.2	27.1	86.8 86.7	86.8	6.3 6.3	6.3		10.5 10.9	10.7		9.0 7.5	8.3	
					Bottom	7.1	23.7 23.8	23.8	8.0 8.0	8.0	27.0 27.1	27.0	87.3 86.8	87.1	6.3 6.3	6.3		10.6 10.4	10.5		9.5 8.9	9.2	
4-Dec-15	Cloudy	Moderate	07:26	7.9	Surface	1.0	23.0 22.9	23.0	8.2 8.1	8.2	25.8 25.8	25.8	87.8 87.7	87.8	6.3 6.3	6.3	6.3	7.7 7.4	7.6	8.9	4.6 4.6	4.6	4.8
					Middle	4.0	23.4 23.6	23.5	8.1 8.1	8.1	28.5 27.4	27.9	85.8 85.5	85.7	6.2 6.3	6.2		9.4 9.5	9.5		4.9 4.5	4.7	
					Bottom	6.9	23.4 23.7	23.6	8.1 8.1	8.1	30.2 29.9	30.1	84.7 84.7	84.7	6.1 6.1	6.1		9.4 9.6	9.5		4.3 5.9	5.1	
7-Dec-15	Cloudy	Moderate	11:16	8.6	Surface	1.0	21.9 21.9	21.9	8.2 8.2	8.2	29.0 29.0	29.0	87.6 90.4	89.0	6.5 6.7	6.6	6.6	10.9 10.4	10.7	11.1	5.7 5.6	5.7	6.1
					Middle	4.3	22.1 22.1	22.1	8.2 8.2	8.2	29.2 29.2	29.2	90.8 88.5	89.7	6.7 6.5	6.6		11.2 11.2	11.2		6.5 6.3	6.4	
					Bottom	7.6	22.2 21.9	22.1	8.1 8.2	8.2	29.4 29.2	29.3	90.2 87.7	89.0	6.6 6.5	6.6		11.2 11.3	11.3		6.8 5.6	6.2	
9-Dec-15	Rainy	Moderate	12:45	8.9	Surface	1.0	21.4 21.4	21.4	8.2 8.2	8.2	30.2 30.2	30.2	86.4 85.6	86.0	6.4 6.4	6.4	6.4	11.2 10.2	10.7	10.9	9.0 9.7	9.4	9.7
					Middle	4.5	21.4 21.4	21.4	8.2 8.2	8.2	30.2 30.2	30.2	87.2 86.1	86.7	6.5 6.4	6.4		10.8 11.0	10.9		9.6 10.0	9.8	
					Bottom	7.9	21.4 21.4	21.4	8.2 8.2	8.2	30.3 30.3	30.3	90.7 85.3	88.0	6.7 6.3	6.5		11.1 11.3	11.2		10.5 9.4	10.0	
11-Dec-15	Sunny	Moderate	11:39	8.9	Surface	1.0	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	83.6 83.7	83.7	6.2 6.2	6.2	6.2	8.8 8.7	8.8	9.0	8.8 8.7	8.8	9.2
					Middle	4.5	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	83.2 83.3	83.3	6.2 6.2	6.2		9.2 9.3	9.3		8.7 9.4	9.1	
					Bottom	7.9	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	83.2 83.6	83.4	6.2 6.2	6.2		9.0 8.7	8.9		10.2 9.0	9.6	
14-Dec-15	Rainy	Moderate	13:56	8.4	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.1	30.1	88.6 88.6	88.6	6.6 6.6	6.6	6.6	12.2 12.4	12.3	12.4	13.2 13.6	13.4	14.0
					Middle	4.2	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.1	30.1	88.6 88.3	88.5	6.6 6.5	6.5		12.4 12.5	12.5		14.4 13.7	14.1	
					Bottom	7.4	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.1	30.1	88.4 88.2	88.3	6.5 6.5	6.5		12.1 12.6	12.4		14.9 13.8	14.4	
16-Dec-15	Sunny	Moderate	15:20	8.9	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	26.4 26.3	26.3	88.8 88.7	88.8	6.9 6.9	6.9	6.9	9.2 9.0	9.1	9.0	11.9 10.6	11.3	12.8
					Middle	4.5	20.3 20.3	20.3	8.3 8.2	8.3	26.3 26.4	26.4	88.8 88.6	88.7	6.9 6.9	6.9		8.7 9.6	9.2		12.8 13.4	13.1	
					Bottom	7.9	20.3 20.3	20.3	8.2 8.3	8.3	26.4 26.3	26.4	88.4 88.4	88.4	6.8 6.8	6.8		9.1 8.5	8.8		13.6 14.3	14.0	
18-Dec-15	Sunny	Moderate	11:40	8.6	Surface	1.0	18.9 19.0	18.9	8.3 8.3	8.3	28.8 28.9	28.9	89.5 89.7	89.6	7.0 7.0	7.0	7.0	5.9 5.6	5.8	5.8	7.2 8.0	7.6	9.0
					Middle	4.3	19.0 19.1	19.1	8.3 8.3	8.3	29.1 29.3	29.2	89.7 89.5	89.6	7.0 7.0	7.0		5.8 5.8	5.8		9.9 9.4	9.7	
					Bottom	7.6	19.0 19.1	19.0	8.3 8.3	8.3	29.2 29.6	29.4	89.5 90.0	89.8	7.0 7.0	7.0		5.8 5.8	5.8		10.3 9.3	9.8	
21-Dec-15	Cloudy	Moderate	14:07	8.6	Surface	1.0	19.2 19.2	19.2	8.3 8.3	8.3	29.5 29.7	29.6	89.3 88.2	88.8	6.9 6.8	6.9	6.9	4.5 5.0	4.8	5.2	4.4 5.3	4.9	5.3
					Middle	4.3	19.1 19.1	19.1	8.4 8.3	8.4	29.7 29.8	29.8	89.0 87.0	88.0	6.9 6.8	6.8		5.1 5.7	5.4		4.9 3.7	4.3	
					Bottom	7.6	19.1 19.1	19.1	8.3 8.4	8.4	29.7 29.8	29.8	89.9 87.3	88.6	7.0 6.8	6.9		5.3 5.3	5.3		7.0 6.3	6.7	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	12:10	8.7	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.7 29.7	29.7	89.1 89.3	89.2	6.8 6.9	6.9	6.9	7.8 7.7	7.8	7.8	11.5 10.7	11.1	11.8
					Middle	4.4	19.7 19.7	19.7	8.2 8.2	8.2	29.8 29.8	29.8	88.9 89.4	89.2	6.8 6.9	6.8		7.8 7.8	7.8		11.5 9.7	10.6	
					Bottom	7.7	19.7 19.7	19.7	8.2 8.2	8.2	29.9 29.8	29.8	89.6 89.3	89.5	6.9 6.9	6.9		7.8 7.8	7.8		14.3 13.0	13.7	
25-Dec-15	Cloudy	Moderate	11:51	8.3	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	28.5 28.5	28.5	90.2 89.9	90.1	6.9 6.9	6.9	6.9	4.6 4.7	4.7	4.7	5.3 3.7	4.5	4.2
					Middle	4.2	20.3 20.3	20.3	8.2 8.2	8.2	28.6 28.6	28.6	90.2 90.1	90.2	6.9 6.9	6.9		4.7 4.6	4.7		3.7 3.7	3.7	
					Bottom	7.3	20.4 20.3	20.4	8.2 8.2	8.2	28.6 28.6	28.6	90.7 90.3	90.5	6.9 6.9	6.9		4.7 4.6	4.7		4.0 5.0	4.5	
28-Dec-15	Sunny	Moderate	13:46	8.5	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.3 28.3	28.3	87.2 87.4	87.3	6.8 6.8	6.8	6.8	8.2 7.9	8.1	8.1	8.8 9.2	9.0	11.3
					Middle	4.3	19.3 19.3	19.3	8.2 8.2	8.2	28.3 28.3	28.3	87.3 86.7	87.0	6.8 6.8	6.8		8.2 8.0	8.1		11.9 12.2	12.1	
					Bottom	7.5	19.3 19.3	19.3	8.2 8.2	8.2	28.3 28.3	28.3	86.6 87.4	87.0	6.8 6.8	6.8		7.9 8.2	8.1		12.8 12.7	12.8	
30-Dec-15	Cloudy	Moderate	14:44	8.8	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.9 28.9	28.9	89.4 88.8	89.1	7.0 6.9	6.9	6.9	9.8 10.0	9.9	9.9	12.7 12.0	12.4	12.1
					Middle	4.4	19.3 19.3	19.3	8.2 8.2	8.2	28.9 28.9	28.9	89.0 88.2	88.6	6.9 6.9	6.9		9.8 9.7	9.8		10.9 11.8	11.4	
					Bottom	7.8	19.3 19.3	19.3	8.3 8.3	8.3	28.9 28.8	28.9	88.3 88.6	88.5	6.9 6.9	6.9		9.9 10.0	10.0		12.6 12.3	12.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	13:09	8.6	Surface	1.0	23.7 23.8	23.7	8.1 8.1	8.1	25.7 25.6	25.6	88.0 88.5	88.3	6.4 6.5	6.4	6.4	10.5 10.5	10.5	10.5	9.2 9.8	9.5	10.4
					Middle	4.3	23.6 23.6	23.6	8.1 8.1	8.1	25.7 25.8	25.7	88.1 87.7	87.9	6.5 6.4	6.4		10.6 10.4	10.5		11.3 10.8	11.1	
					Bottom	7.6	23.6 23.6	23.6	8.1 8.1	8.1	25.8 25.8	25.8	89.2 88.0	88.6	6.5 6.4	6.5		10.6 10.6	10.6		10.3 10.6	10.5	
4-Dec-15	Cloudy	Moderate	13:11	8.6	Surface	1.0	22.9 22.9	22.9	8.2 8.2	8.2	26.6 26.5	26.6	83.1 84.5	83.8	6.1 6.2	6.2	6.2	9.7 9.5	9.6	9.6	6.9 6.3	6.6	6.4
					Middle	4.3	23.5 23.6	23.5	8.2 8.2	8.2	29.3 30.0	29.7	84.5 85.1	84.8	6.1 6.1	6.1		9.6 9.5	9.6		6.6 5.9	6.3	
					Bottom	7.6	23.4 23.1	23.3	8.1 8.2	8.2	32.3 32.5	32.4	87.7 85.8	86.8	6.2 6.1	6.1		9.6 9.3	9.5		6.7 6.1	6.4	
7-Dec-15	Cloudy	Moderate	15:11	8.6	Surface	1.0	22.4 22.4	22.4	8.2 8.2	8.2	30.6 30.6	30.6	84.2 85.6	84.9	6.1 6.2	6.1	6.1	5.3 5.2	5.3	5.3	6.0 6.1	6.1	5.7
					Middle	4.3	22.6 22.6	22.6	8.2 8.2	8.2	31.1 31.0	31.1	83.9 83.6	83.8	6.1 6.1	6.1		5.2 5.1	5.2		4.9 5.2	5.1	
					Bottom	7.6	22.5 22.6	22.6	8.2 8.2	8.2	31.6 31.4	31.5	83.1 83.5	83.3	6.0 6.0	6.0		5.4 5.3	5.4		5.7 5.9	5.8	
9-Dec-15	Rainy	Moderate	16:00	8.4	Surface	1.0	21.4 21.4	21.4	8.1 8.1	8.1	28.3 28.3	28.3	84.5 84.6	84.6	6.3 6.3	6.3	6.3	8.8 8.8	8.8	8.8	6.8 6.4	6.6	6.6
					Middle	4.2	21.5 21.5	21.5	8.1 8.1	8.1	28.5 28.5	28.5	83.9 85.7	84.8	6.3 6.4	6.3		8.8 8.7	8.8		7.0 7.1	7.1	
					Bottom	7.4	21.5 21.5	21.5	8.1 8.1	8.1	28.5 28.5	28.5	86.0 84.0	85.0	6.4 6.3	6.4		8.8 8.7	8.8		5.7 6.7	6.2	
11-Dec-15	Sunny	Moderate	08:32	8.7	Surface	1.0	21.3 21.4	21.4	8.2 8.2	8.2	30.4 30.4	30.4	84.9 88.0	86.5	6.3 6.5	6.4	6.5	7.0 7.4	7.2	7.5	7.0 7.0	7.0	8.8
					Middle	4.4	21.4 21.4	21.4	8.2 8.2	8.2	30.4 30.4	30.4	85.2 89.8	87.5	6.3 6.7	6.5		7.3 7.7	7.5		8.0 7.1	7.6	
					Bottom	7.7	21.3 21.4	21.3	8.2 8.2	8.2	30.4 30.4	30.4	93.1 86.2	89.7	6.9 6.4	6.7		8.0 7.5	7.8		11.4 12.2	11.8	
14-Dec-15	Rainy	Moderate	10:45	8.5	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.0 30.0	30.0	94.8 90.0	92.4	7.0 6.7	6.8	6.8	9.8 9.3	9.6	9.7	10.6 10.8	10.7	10.9
					Middle	4.3	21.6 21.6	21.6	8.2 8.2	8.2	30.0 30.1	30.0	91.8 90.1	91.0	6.8 6.7	6.7		9.7 9.6	9.7		10.2 11.6	10.9	
					Bottom	7.5	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.0	30.0	90.0 90.8	90.4	6.7 6.7	6.7		9.6 9.8	9.7		10.8 11.1	11.0	
16-Dec-15	Sunny	Moderate	12:23	8.7	Surface	1.0	20.3 20.3	20.3	8.1 8.1	8.1	27.4 27.4	27.4	90.0 90.2	90.1	6.9 7.0	6.9	7.0	13.2 12.5	12.9	12.9	11.6 11.8	11.7	14.2
					Middle	4.4	20.3 20.3	20.3	8.1 8.1	8.1	27.3 27.4	27.4	91.3 91.8	91.6	7.0 7.1	7.0		12.8 12.9	12.9		14.3 14.4	14.4	
					Bottom	7.7	20.3 20.3	20.3	8.1 8.1	8.1	27.2 27.4	27.3	88.1 88.4	88.3	6.8 6.8	6.8		12.8 13.2	13.0		16.0 16.8	16.4	
18-Dec-15	Cloudy	Moderate	06:20	8.2	Surface	1.0	19.1 19.1	19.1	8.2 8.2	8.2	28.7 28.7	28.7	88.4 88.0	88.2	6.9 6.9	6.9	6.9	8.8 8.5	8.7	8.6	7.1 7.1	7.1	7.2
					Middle	4.1	19.3 19.2	19.2	8.2 8.2	8.2	28.9 28.8	28.9	88.0 88.1	88.1	6.8 6.9	6.9		8.6 8.5	8.6		7.0 7.7	7.4	
					Bottom	7.2	19.2 19.3	19.2	8.2 8.2	8.2	29.0 29.1	29.1	88.6 88.7	88.7	6.9 6.9	6.9		8.6 8.5	8.6		7.5 6.7	7.1	
21-Dec-15	Sunny	Moderate	10:16	8.4	Surface	1.0	18.8 18.8	18.8	8.2 8.2	8.2	30.4 30.4	30.4	91.1 90.1	90.6	7.1 7.0	7.0	7.1	5.8 5.5	5.7	5.7	4.5 4.4	4.5	4.8
					Middle	4.2	18.8 18.8	18.8	8.2 8.2	8.2	30.5 30.5	30.5	92.4 92.5	92.5	7.2 7.2	7.2		5.8 5.7	5.8		3.0 4.8	3.9	
					Bottom	7.4	18.8 18.8	18.8	8.2 8.2	8.2	30.5 30.4	30.5	89.6 92.2	90.9	7.0 7.2	7.1		5.6 5.8	5.7		6.7 5.5	6.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	15:41	8.7	Surface	1.0	19.9 19.9	19.9	8.3 8.3	8.3	30.3 30.4	30.3	90.0 89.5	89.8	6.9 6.8	6.8	6.8	8.4 8.6	8.5	8.7	12.2 10.3	11.3	9.9
					Middle	4.4	19.9 19.9	19.9	8.3 8.3	8.3	30.4 30.5	30.4	89.1 89.3	89.2	6.8 6.8	6.8		8.7 8.6	8.7		9.1 10.3	9.7	
					Bottom	7.7	19.9 19.9	19.9	8.3 8.3	8.3	30.4 30.5	30.5	89.2 89.6	89.4	6.8 6.8	6.8		8.9 8.9	8.9		7.8 9.4	8.6	
25-Dec-15	Cloudy	Moderate	08:36	8.4	Surface	1.0	20.4 20.3	20.3	8.2 8.2	8.2	28.5 28.5	28.5	93.5 91.0	92.3	7.1 7.0	7.1	7.1	4.5 4.4	4.5	4.6	4.6 5.1	4.9	5.1
					Middle	4.2	20.3 20.3	20.3	8.2 8.2	8.2	28.5 28.5	28.5	90.5 93.3	91.9	6.9 7.1	7.0		4.6 4.7	4.7		4.3 5.8	5.1	
					Bottom	7.4	20.4 20.4	20.4	8.2 8.2	8.2	28.6 28.6	28.6	91.5 92.3	91.9	7.0 7.0	7.0		4.6 4.8	4.7		5.0 5.4	5.2	
28-Dec-15	Sunny	Moderate	10:50	9.4	Surface	1.0	19.2 19.2	19.2	8.2 8.2	8.2	27.9 28.0	27.9	88.5 88.3	88.4	6.9 6.9	6.9	7.0	9.1 8.9	9.0	9.3	12.0 11.1	11.6	11.9
					Middle	4.7	19.2 19.2	19.2	8.2 8.2	8.2	27.9 28.0	28.0	91.0 87.8	89.4	7.1 6.9	7.0		9.5 9.4	9.5		11.3 11.8	11.6	
					Bottom	8.4	19.2 19.2	19.2	8.2 8.2	8.2	27.9 27.9	27.9	90.3 87.6	89.0	7.1 6.9	7.0		9.2 9.3	9.3		12.5 12.6	12.6	
30-Dec-15	Cloudy	Moderate	12:03	8.7	Surface	1.0	19.2 19.2	19.2	8.2 8.2	8.2	28.2 28.2	28.2	89.1 89.6	89.4	7.0 7.0	7.0	7.0	7.1 6.9	7.0	7.1	8.1 8.4	8.3	8.2
					Middle	4.4	19.2 19.2	19.2	8.2 8.2	8.2	28.3 28.3	28.3	88.5 90.1	89.3	6.9 7.0	7.0		6.8 7.1	7.0		8.0 8.0	8.0	
					Bottom	7.7	19.2 19.2	19.2	8.2 8.2	8.2	28.3 28.3	28.3	88.6 91.2	89.9	6.9 7.1	7.0		6.9 7.4	7.2		8.2 8.4	8.3	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	17:07	3.4	Surface	1.0	24.0 23.9	23.9	8.0 8.0	8.0	27.7 27.7	27.7	89.1 88.9	89.0	6.4 6.4	6.4	6.4	8.6 8.7	8.7	8.7	6.8 6.1	6.5	6.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	23.8 23.7	23.8	8.0 8.0	8.0	27.8 27.9	27.9	88.5 88.0	88.3	6.4 6.3	6.4		6.4	8.6 8.8		8.7	5.9 6.5		6.2			
4-Dec-15	Cloudy	Moderate	07:06	3.1	Surface	1.0	22.6 22.7	22.7	8.1 8.1	8.1	24.5 24.5	24.5	89.5 88.4	89.0	6.7 6.6	6.7	6.7	10.4 10.5	10.5	10.6	3.8 4.7	4.3	5.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	22.7 22.9	22.8	8.1 8.1	8.1	25.7 25.2	25.5	90.4 97.2	93.8	6.7 7.2	7.0		7.0	10.8 10.4		10.6	5.4 7.3		6.4			
7-Dec-15	Cloudy	Moderate	10:59	3.2	Surface	1.0	22.1 22.2	22.2	8.2 8.2	8.2	29.1 29.0	29.1	86.8 87.4	87.1	6.4 6.4	6.4	6.4	5.6 5.7	5.7	5.8	3.5 4.1	3.8	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	22.3 22.2	22.2	8.1 8.2	8.2	29.2 29.2	29.2	88.8 87.4	88.1	6.5 6.4	6.5		6.5	5.7 5.9		5.8	5.6 6.4		6.0			
9-Dec-15	Rainy	Moderate	12:31	3.2	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	29.9 29.9	29.9	86.1 85.8	86.0	6.4 6.4	6.4	6.4	4.1 4.2	4.2	4.3	4.0 5.9	5.0	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.2	21.5 21.5	21.5	8.2 8.2	8.2	29.9 29.9	29.9	85.9 86.5	86.2	6.4 6.4	6.4		6.4	4.2 4.3		4.3	4.2 5.2		4.7			
11-Dec-15	Sunny	Moderate	11:58	3.4	Surface	1.0	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	83.9 83.2	83.6	6.2 6.2	6.2	6.2	8.5 7.5	8.0	7.8	6.2 6.6	6.4	6.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.4	21.4 21.4	21.4	8.2 8.2	8.2	30.6 30.6	30.6	83.7 83.4	83.6	6.2 6.2	6.2		6.2	7.8 7.3		7.6	7.4 7.4		7.4			
14-Dec-15	Rainy	Moderate	14:13	3.2	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	29.7 29.7	29.7	95.5 94.2	94.9	7.1 7.0	7.0	7.0	5.8 5.7	5.8	5.9	5.2 4.3	4.8	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.2	21.5 21.5	21.5	8.2 8.2	8.2	29.9 29.8	29.9	97.2 95.1	96.2	7.2 7.1	7.1		7.1	5.8 5.9		5.9	5.3 5.5		5.4			
16-Dec-15	Sunny	Moderate	15:38	3.4	Surface	1.0	20.4 20.4	20.4	8.2 8.2	8.2	26.6 26.7	26.7	89.9 89.6	89.8	6.9 6.9	6.9	6.9	7.9 7.6	7.8	7.8	10.1 10.2	10.2	10.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.4	20.4 20.4	20.4	8.2 8.2	8.2	26.7 26.7	26.7	89.5 90.2	89.9	6.9 7.0	6.9		6.9	7.7 7.6		7.7	10.9 11.5		11.2			
18-Dec-15	Sunny	Moderate	11:57	3.2	Surface	1.0	18.9 18.9	18.9	8.2 8.2	8.2	28.7 28.8	28.7	90.4 90.3	90.4	7.1 7.1	7.1	7.1	6.1 6.2	6.2	6.2	7.4 7.2	7.3	8.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.2	18.8 18.9	18.9	8.2 8.2	8.2	28.8 28.7	28.8	90.1 90.3	90.2	7.1 7.1	7.1		7.1	6.1 6.3		6.2	8.6 9.5		9.1			
21-Dec-15	Cloudy	Moderate	14:26	3.2	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	29.7 29.7	29.7	90.9 90.7	90.8	7.0 7.0	7.0	7.0	6.7 7.2	7.0	7.3	4.5 3.5	4.0	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	2.2	19.3 19.3	19.3	8.2 8.2	8.2	29.7 29.7	29.7	90.6 90.5	90.6	7.0 7.0	7.0		7.0	7.1 7.8		7.5	4.2 5.5		4.9			

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-Dec-15	Sunny	Moderate	11:53	3.2	Surface	1.0	19.9 19.9	19.9	8.2 8.2	8.2	30.0 30.0	30.0	92.2 93.3	92.8	7.0 7.1	7.1	7.1	3.9 3.9	3.9	3.9	5.6 6.1	5.9	6.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	19.8 19.9	19.8	8.2 8.2	8.2	30.2 30.0	30.1	92.7 92.3	92.5	7.1 7.0	7.1		7.1	3.9 3.8		3.9	7.1		3.9 7.1	6.2	7.1	
25-Dec-15	Cloudy	Moderate	12:07	3.3	Surface	1.0	20.2 20.3	20.3	8.2 8.2	8.2	28.4 28.4	28.4	91.5 90.9	91.2	7.0 7.0	7.0	7.0	3.7 3.7	3.7	3.8	3.5 3.5	3.5	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.3	20.3 20.3	20.3	8.2 8.2	8.2	28.5 28.5	28.5	91.2 91.2	91.2	7.0 7.0	7.0		7.0	3.8 3.7		3.8	7.0		2.3 3.4	2.9	3.4	
28-Dec-15	Sunny	Moderate	14:00	3.2	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.2 28.2	28.2	88.0 87.9	88.0	6.9 6.9	6.9	6.9	5.8 6.2	6.0	6.0	6.7 5.9	6.3	7.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	19.3 19.3	19.3	8.2 8.2	8.2	28.2 28.2	28.2	87.5 87.3	87.4	6.8 6.8	6.8		6.8	5.9 6.0		6.0	6.8		8.5 7.9	8.2	7.9	
30-Dec-15	Cloudy	Moderate	15:00	3.4	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.9 28.9	28.9	88.9 89.5	89.2	6.9 7.0	6.9	6.9	5.5 6.1	5.8	5.7	7.0 6.0	6.5	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.4	19.3 19.3	19.3	8.2 8.2	8.2	28.9 28.9	28.9	89.3 88.9	89.1	6.9 6.9	6.9		6.9	5.3 5.8		5.6	6.9		7.0 5.9	6.5	5.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	12:51	3.2	Surface	1.0	23.7 23.8	23.8	8.1 8.1	8.1	25.7 25.7	25.7	89.8 90.2	90.0	6.6 6.6	6.6	6.6	9.9 9.6	9.8	9.9	9.5 10.2	9.9	10.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	23.7 23.7	23.7	8.1 8.1	8.1	25.7 25.8	25.8	89.8 90.5	90.2	6.6 6.6	6.6		9.9 10.0	10.0		6.6	9.9 10.2		10.0	6.6	10.2 10.2
4-Dec-15	Cloudy	Moderate	13:26	3.2	Surface	1.0	22.6 22.6	22.6	8.1 8.1	8.1	26.3 26.3	26.3	92.4 89.8	91.1	6.9 6.7	6.8	6.8	4.2 4.3	4.3	4.3	5.0 4.6	4.8	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	22.6 22.6	22.6	8.1 8.1	8.1	26.4 26.4	26.4	92.6 90.1	91.4	6.9 6.7	6.8		4.3 4.3	4.3		6.8	4.3 4.3		4.3	6.8	3.6 5.0
7-Dec-15	Cloudy	Moderate	15:27	3.3	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	30.2 30.2	30.2	90.6 90.2	90.4	6.6 6.6	6.6	6.6	5.2 5.3	5.3	5.3	6.6 6.0	6.3	6.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	22.3 22.5	22.4	8.2 8.2	8.2	30.2 30.2	30.2	90.0 88.4	89.2	6.6 6.4	6.5		5.3 5.3	5.3		6.5	5.3 5.3		5.3	6.5	6.4 6.5
9-Dec-15	Rainy	Moderate	16:17	3.2	Surface	1.0	21.3 21.3	21.3	8.1 8.1	8.1	28.8 28.8	28.8	85.9 86.2	86.1	6.4 6.5	6.4	6.4	4.4 4.3	4.4	4.4	4.6 4.0	4.3	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	21.3 21.4	21.4	8.1 8.1	8.1	28.9 28.9	28.9	86.1 85.9	86.0	6.5 6.4	6.4		4.4 4.4	4.4		6.4	4.4 4.4		4.4	6.4	6.2 5.4
11-Dec-15	Sunny	Moderate	08:11	3.4	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.7	30.7	84.5 84.4	84.5	6.2 6.2	6.2	6.2	6.2 6.6	6.4	7.2	4.7 5.2	5.0	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	21.6 21.7	21.6	8.2 8.2	8.2	30.8 30.8	30.8	84.5 84.3	84.4	6.2 6.2	6.2		7.7 8.0	7.9		6.2	7.7 8.0		7.9	6.2	5.3 5.2
14-Dec-15	Rainy	Moderate	10:28	3.3	Surface	1.0	21.5 21.5	21.5	8.1 8.1	8.1	30.0 30.0	30.0	92.1 91.1	91.6	6.8 6.8	6.8	6.8	16.4 16.5	16.5	16.5	13.2 13.9	13.6	13.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	21.5 21.5	21.5	8.1 8.1	8.1	30.0 30.0	30.0	95.6 91.4	93.5	7.1 6.8	6.9		16.5 16.4	16.5		6.9	16.5 16.4		16.5	6.9	12.9 12.6
16-Dec-15	Sunny	Moderate	12:00	3.3	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.4	27.4	90.6 91.4	91.0	6.9 7.0	7.0	7.0	6.0 6.3	6.2	6.4	8.8 8.5	8.7	9.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.5	27.5	91.0 91.5	91.3	7.0 7.0	7.0		6.4 6.8	6.6		7.0	6.4 6.8		6.6	7.0	9.6 9.4
18-Dec-15	Cloudy	Moderate	06:02	3.3	Surface	1.0	18.9 18.8	18.9	8.2 8.2	8.2	28.4 28.2	28.3	90.6 92.7	91.7	7.1 7.3	7.2	7.2	7.6 7.5	7.6	7.7	4.2 4.6	4.4	4.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	18.9 19.0	19.0	8.1 8.2	8.2	28.5 28.6	28.5	96.9 91.9	94.4	7.6 7.2	7.4		7.7 7.6	7.7		7.4	7.7 7.6		7.7	7.4	3.3 3.6
21-Dec-15	Sunny	Moderate	09:53	3.3	Surface	1.0	18.9 18.9	18.9	8.2 8.2	8.2	30.0 30.0	30.0	92.2 89.7	91.0	7.2 7.0	7.1	7.1	3.7 3.8	3.8	4.0	6.4 6.9	6.7	7.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	18.9 18.9	18.9	8.2 8.2	8.2	30.0 30.0	30.0	93.7 90.7	92.2	7.3 7.1	7.2		4.0 4.2	4.1		7.2	4.0 4.2		4.1	7.2	9.0 7.3

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	15:59	3.2	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.3 30.3	30.3	92.6 94.8	93.7	7.0 7.2	7.1	7.1	7.3 7.0	7.2	7.1	8.7 7.4	8.1	8.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	20.3 20.4	20.3	8.2 8.2	8.2	30.4 30.3	30.4	95.1 93.2	94.2	7.2 7.0	7.1		7.1	7.0 7.0		7.0	10.3 9.1		9.7		
25-Dec-15	Cloudy	Moderate	08:16	3.1	Surface	1.0	20.1 20.2	20.2	8.1 8.1	8.1	28.1 28.2	28.1	96.3 93.1	94.7	7.4 7.2	7.3	7.3	5.5 5.2	5.4	5.4	6.0 6.3	6.2	6.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.1	20.2 20.2	20.2	8.1 8.1	8.1	28.3 28.3	28.3	95.2 96.5	95.9	7.3 7.4	7.4		7.4	5.5 5.3		5.4	5.7 6.5		6.1		
28-Dec-15	Sunny	Moderate	10:26	3.2	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.1 28.0	28.0	88.3 90.0	89.2	6.9 7.0	7.0	7.0	9.9 9.8	9.9	9.8	11.8 12.9	12.4	13.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.2	19.3 19.3	19.3	8.2 8.2	8.2	28.1 28.0	28.0	89.2 91.5	90.4	7.0 7.2	7.1		7.1	9.7 9.6		9.7	14.3 13.3		13.8		
30-Dec-15	Cloudy	Moderate	11:41	3.2	Surface	1.0	19.3 19.3	19.3	8.2 8.2	8.2	28.3 28.3	28.3	89.1 88.0	88.6	7.0 6.9	6.9	6.9	5.0 5.1	5.1	5.0	5.9 5.0	5.5	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.2	19.3 19.3	19.3	8.2 8.2	8.2	28.3 28.3	28.3	88.2 87.9	88.1	6.9 6.9	6.9		6.9	5.0 4.7		4.9	5.3 6.0		5.7		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	17:28	3.6	Surface	1.0	23.8 23.8	23.8	8.1 8.1	8.1	27.4 27.4	27.4	88.4 88.3	88.4	6.4 6.4	6.4	6.4	11.4 11.3	11.4	11.6	7.5 7.7	7.6	7.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	23.9 23.8	23.9	8.1 8.1	8.1	27.5 27.5	27.5	88.5 88.3	88.4	6.4 6.4	6.4		6.4	11.8 11.5		11.7	6.4		11.8 11.5	11.7	8.4 6.8	7.6
4-Dec-15	Cloudy	Moderate	06:44	3.6	Surface	1.0	22.6 23.0	22.8	8.1 8.1	8.1	25.0 24.7	24.8	88.3 87.6	88.0	6.6 6.5	6.6	6.6	8.5 8.8	8.7	8.8	3.5 4.0	3.8	3.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	23.6 22.9	23.3	8.1 8.1	8.1	24.9 27.4	26.1	86.6 88.5	87.6	6.4 6.5	6.4		6.4	8.8 8.7		8.8	6.4		8.8 8.7	8.8	3.2 3.3	3.3
7-Dec-15	Cloudy	Moderate	10:35	3.9	Surface	1.0	22.1 22.2	22.1	8.2 8.2	8.2	28.6 28.7	28.6	84.4 85.1	84.8	6.2 6.3	6.3	6.3	5.3 5.5	5.4	5.5	5.2 5.4	5.3	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	22.6 22.2	22.4	8.1 8.1	8.1	29.2 29.5	29.4	87.8 86.6	87.2	6.4 6.4	6.4		6.4	5.5 5.4		5.5	6.4		5.5 5.4	5.5	5.0 4.8	4.9
9-Dec-15	Rainy	Moderate	12:06	4.1	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	29.9 29.9	29.9	88.7 90.1	89.4	6.6 6.7	6.6	6.6	3.2 3.1	3.2	3.3	3.4 2.6	3.0	3.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	21.6 21.6	21.6	8.2 8.2	8.2	30.0 30.0	30.0	88.9 92.5	90.7	6.6 6.8	6.7		6.7	3.2 3.3		3.3	6.7		3.2 3.3	3.3	4.6 3.1	3.9
11-Dec-15	Sunny	Moderate	12:31	3.6	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.9 30.8	30.8	86.4 86.3	86.4	6.4 6.4	6.4	6.4	5.8 5.8	5.8	5.6	6.2 6.2	6.2	6.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	21.6 21.6	21.6	8.2 8.2	8.2	31.0 30.9	30.9	86.1 85.8	86.0	6.3 6.3	6.3		6.3	5.1 5.7		5.4	6.3		5.1 5.7	5.4	7.5 6.8	7.2
14-Dec-15	Rainy	Moderate	14:35	3.9	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	28.4 28.6	28.5	88.7 88.6	88.7	6.6 6.6	6.6	6.6	5.8 5.9	5.9	5.9	5.2 4.8	5.0	5.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	21.5 21.6	21.6	8.2 8.1	8.2	29.4 30.0	29.7	89.0 88.7	88.9	6.6 6.6	6.6		6.6	5.9 5.8		5.9	6.6		5.9 5.8	5.9	4.5 5.5	5.0
16-Dec-15	Sunny	Moderate	16:11	3.7	Surface	1.0	20.6 20.6	20.6	8.2 8.2	8.2	26.8 26.8	26.8	89.0 89.5	89.3	6.8 6.9	6.9	6.9	8.9 8.5	8.7	9.1	8.4 8.6	8.5	8.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	20.7 20.6	20.7	8.2 8.2	8.2	27.2 27.0	27.1	89.7 88.9	89.3	6.9 6.8	6.8		6.8	9.8 8.9		9.4	6.8		9.8 8.9	9.4	8.6 9.3	9.0
18-Dec-15	Sunny	Moderate	12:21	4.0	Surface	1.0	19.8 19.7	19.7	8.2 8.2	8.2	29.0 29.0	29.0	86.1 86.0	86.1	6.6 6.6	6.6	6.6	12.0 11.2	11.6	11.6	3.2 3.3	3.3	3.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.0	19.9 20.0	19.9	8.2 8.2	8.2	29.8 29.8	29.8	87.1 87.3	87.2	6.7 6.7	6.7		6.7	11.9 11.1		11.5	6.7		11.9 11.1	11.5	3.9 4.4	4.2
21-Dec-15	Cloudy	Moderate	15:01	3.7	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.9 29.9	29.9	91.4 86.9	89.2	7.0 6.7	6.8	6.8	7.6 8.2	7.9	7.8	2.2 3.6	2.9	4.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	19.7 19.7	19.7	8.2 8.2	8.2	30.0 29.9	30.0	91.1 88.9	90.0	7.0 6.8	6.9		6.9	7.2 7.9		7.6	6.9		7.2 7.9	7.6	5.2 4.9	5.1

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	11:27	4.0	Surface	1.0	19.9 19.9	19.9	8.2 8.2	8.2	30.0 30.1	30.0	93.4 91.9	92.7	7.1 7.0	7.1	7.1	6.4 6.5	6.5	6.5	5.9 4.1	5.0	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.0	19.9 19.9	19.9	8.2 8.2	8.2	30.2 30.1	30.2	93.4 93.5	93.5	7.1 7.1	7.1		7.1	6.5 6.5		6.5	7.1		5.4 5.5	5.5	5.5
25-Dec-15	Cloudy	Moderate	12:29	4.3	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	27.0 27.1	27.1	92.2 89.4	90.8	7.1 6.9	7.0	7.0	5.2 5.3	5.3	5.3	6.0 5.1	5.6	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.3	20.4 20.1	20.2	8.1 8.2	8.2	28.2 28.6	28.4	92.8 90.1	91.5	7.1 6.9	7.0		7.0	5.2 5.4		5.3	7.0		4.5 4.5	4.5	4.5
28-Dec-15	Sunny	Moderate	14:23	3.9	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.1 28.1	28.1	87.0 87.1	87.1	6.8 6.8	6.8	6.8	7.3 7.2	7.3	7.3	9.3 9.0	9.2	9.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	19.4 19.4	19.4	8.2 8.2	8.2	28.1 28.1	28.1	86.6 87.1	86.9	6.7 6.8	6.8		6.8	7.1 7.4		7.3	6.8		9.0 9.9	9.5	9.5
30-Dec-15	Cloudy	Moderate	15:34	3.8	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.6 28.6	28.6	91.2 90.3	90.8	7.1 7.0	7.0	7.0	5.4 5.1	5.3	5.8	6.4 5.6	6.0	5.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	19.5 19.6	19.6	8.2 8.2	8.2	28.8 28.9	28.9	91.9 94.2	93.1	7.1 7.3	7.2		7.2	6.0 6.3		6.2	7.2		5.1 5.8	5.5	5.5

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	12:29	4.1	Surface	1.0	23.7 23.6	23.6	8.1 8.1	8.1	25.4 25.4	25.4	89.2 90.1	89.7	6.5 6.6	6.6	6.6	8.0 8.3	8.2	8.2	4.1 3.7	3.9	4.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	23.6 23.7	23.6	8.1 8.1	8.1	25.7 25.4	25.6	88.6 89.6	89.1	6.5 6.6	6.5		8.2 8.2	8.2		6.5	8.2 8.2		8.2	3.5 5.0	4.3	
4-Dec-15	Cloudy	Moderate	13:48	3.8	Surface	1.0	23.0 23.0	23.0	8.1 8.1	8.1	26.7 26.9	26.8	83.5 84.7	84.1	6.1 6.2	6.2	6.2	10.4 10.9	10.7	10.7	7.2 7.5	7.4	7.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	23.0 23.3	23.2	8.1 8.1	8.1	27.2 27.2	27.2	84.7 82.9	83.8	6.2 6.1	6.1		11.2 10.2	10.7		6.1	11.2 10.2		10.7	7.6 8.1	7.9	
7-Dec-15	Cloudy	Moderate	15:53	4.2	Surface	1.0	22.1 22.1	22.1	8.2 8.2	8.2	29.6 29.8	29.7	88.3 87.1	87.7	6.5 6.4	6.5	6.5	7.8 7.6	7.7	7.7	5.4 4.9	5.2	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.2	22.1 22.5	22.3	8.2 8.1	8.2	30.0 30.2	30.1	88.2 92.1	90.2	6.5 6.7	6.6		7.7 7.7	7.7		6.6	7.7 7.7		7.7	5.2 4.6	4.9	
9-Dec-15	Rainy	Moderate	16:41	4.2	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	29.5 29.5	29.5	85.8 85.6	85.7	6.4 6.4	6.4	6.4	11.2 11.3	11.3	11.4	4.4 4.0	4.2	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.2	21.6 21.9	21.8	8.2 8.2	8.2	29.6 29.8	29.7	85.7 84.5	85.1	6.4 6.2	6.3		11.5 11.4	11.5		6.3	11.5 11.4		11.5	3.1 5.1	4.1	
11-Dec-15	Sunny	Moderate	07:39	3.8	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	30.7 30.7	30.7	93.4 89.3	91.4	6.9 6.6	6.7	6.7	6.1 5.9	6.0	6.2	5.8 5.5	5.7	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	21.5 21.5	21.5	8.2 8.2	8.2	30.7 30.7	30.7	92.3 89.0	90.7	6.8 6.6	6.7		6.4 6.2	6.3		6.7	6.4 6.2		6.3	6.0 6.1	6.1	
14-Dec-15	Rainy	Moderate	10:05	4.0	Surface	1.0	21.5 21.5	21.5	8.1 8.1	8.1	28.4 28.4	28.4	90.3 94.2	92.3	6.8 7.0	6.9	6.9	13.6 13.3	13.5	13.5	10.5 11.6	11.1	12.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.0	21.5 21.5	21.5	8.1 8.1	8.1	28.5 28.7	28.6	90.5 91.0	90.8	6.8 6.8	6.8		13.5 13.3	13.4		6.8	13.5 13.3		13.4	12.1 14.4	13.3	
16-Dec-15	Sunny	Moderate	11:34	3.7	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	27.3 27.3	27.3	91.4 95.6	93.5	7.0 7.3	7.2	7.2	9.0 8.8	8.9	9.1	9.2 10.9	10.1	11.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.7	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.3	27.3	92.8 98.3	95.6	7.1 7.5	7.3		9.3 9.0	9.2		7.3	9.3 9.0		9.2	11.9 13.2	12.6	
18-Dec-15	Cloudy	Moderate	05:40	3.9	Surface	1.0	19.1 19.2	19.1	8.2 8.2	8.2	28.3 28.5	28.4	89.6 89.9	89.8	7.0 7.0	7.0	7.0	4.5 4.5	4.5	4.6	3.2 3.8	3.5	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.9	19.1 19.0	19.0	8.2 8.2	8.2	28.4 29.5	28.9	89.4 91.5	90.5	7.0 7.1	7.1		4.5 4.6	4.6		7.1	4.5 4.6		4.6	4.8 5.9	5.4	
21-Dec-15	Sunny	Moderate	09:22	3.7	Surface	1.0	19.6 19.5	19.6	8.2 8.2	8.2	30.3 30.2	30.3	88.1 86.5	87.3	6.7 6.7	6.7	6.7	3.5 3.5	3.5	3.7	11.3 10.1	10.7	10.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.7	19.5 19.7	19.6	8.2 8.2	8.2	30.4 30.5	30.4	86.7 88.4	87.6	6.7 6.8	6.7		3.7 4.0	3.9		6.7	3.7 4.0		3.9	10.4 10.5	10.5	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	16:28	4.2	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.0 30.1	30.0	92.2 94.2	93.2	7.0 7.1	7.1	7.1	7.8 8.0	7.9	7.9	10.4 10.5	10.5	11.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	20.3 20.3	20.3	8.2 8.2	8.2	30.4 30.1	30.3	94.9 94.1	94.5	7.2 7.1	7.2		7.2	7.8 7.9		7.9	7.2		7.8 7.9	7.9	12.2 10.6
25-Dec-15	Cloudy	Moderate	07:56	4.0	Surface	1.0	20.1 20.0	20.1	8.1 8.1	8.1	27.0 26.9	27.0	92.1 91.6	91.9	7.1 7.1	7.1	7.1	6.7 6.7	6.7	6.8	6.0 6.0	6.0	6.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.0	20.1 20.1	20.1	8.1 8.1	8.1	27.3 27.3	27.3	92.4 94.8	93.6	7.1 7.3	7.2		7.2	6.8 6.7		6.8	7.2		6.8 6.7	6.8	6.3 8.0
28-Dec-15	Sunny	Moderate	09:31	3.9	Surface	1.0	19.4 19.4	19.4	8.1 8.1	8.1	27.9 27.9	27.9	88.3 89.0	88.7	6.9 7.0	6.9	6.9	7.8 7.8	7.8	7.8	5.1 6.2	5.7	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.9	19.4 19.4	19.4	8.1 8.1	8.1	27.9 27.9	27.9	90.7 88.8	89.8	7.1 6.9	7.0		7.0	7.8 7.6		7.7	7.0		7.8 7.6	7.7	4.7 6.3
30-Dec-15	Cloudy	Moderate	11:12	3.8	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.4 28.4	28.4	88.9 88.4	88.7	6.9 6.9	6.9	6.9	15.9 16.1	16.0	15.7	14.3 14.8	14.6	15.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.8	19.4 19.4	19.4	8.2 8.2	8.2	28.5 28.5	28.5	88.3 87.0	87.7	6.9 6.8	6.8		6.8	14.9 15.8		15.4	6.8		14.9 15.8	15.4	16.7 17.0

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	17:41	9.7	Surface	1.0	23.7 23.7	23.7	8.1 8.1	8.1	26.5 26.0	26.3	85.6 83.9	84.8	6.2 6.1	6.2	6.2	6.0 6.0	6.0	6.5	5.4 5.4	5.4	4.7
					Middle	4.9	23.7 23.7	23.7	8.1 8.1	8.1	28.7 28.6	28.7	83.3 88.0	85.7	6.0 6.3	6.2		6.8 6.7	6.8		5.0 4.0	4.5	
					Bottom	8.7	23.7 23.7	23.7	8.1 8.0	8.0	28.8 28.9	28.8	84.7 87.5	86.1	6.1 6.3	6.2		6.7 6.7	6.7		4.0 4.2	4.1	
4-Dec-15	Cloudy	Moderate	06:30	10.6	Surface	1.0	22.8 23.1	23.0	8.1 8.2	8.1	25.6 25.3	25.5	90.4 86.6	88.5	6.5 6.3	6.4	6.4	4.0 4.2	4.1	4.4	3.4 2.8	3.1	3.2
					Middle	5.3	23.9 23.9	23.9	8.1 8.1	8.1	28.7 28.1	28.4	85.0 87.1	86.1	6.1 6.4	6.3		4.5 4.4	4.5		3.4 2.7	3.1	
					Bottom	9.6	23.8 23.9	23.9	8.1 8.1	8.1	30.0 29.9	30.0	84.5 86.6	85.6	6.0 6.3	6.1		4.5 4.4	4.5		3.8 2.8	3.3	
7-Dec-15	Cloudy	Moderate	10:20	9.8	Surface	1.0	22.7 22.8	22.8	8.2 8.2	8.2	30.4 30.4	30.4	90.1 86.0	88.1	6.5 6.2	6.3	6.3	3.3 3.3	3.3	3.3	4.3 4.8	4.6	4.9
					Middle	4.9	22.9 22.9	22.9	8.2 8.2	8.2	30.7 30.7	30.7	85.3 88.0	86.7	6.1 6.3	6.2		3.3 3.2	3.3		4.5 5.4	5.0	
					Bottom	8.8	22.8 22.8	22.8	8.2 8.2	8.2	30.8 30.9	30.8	87.4 84.8	86.1	6.3 6.1	6.2		3.1 3.2	3.2		5.0 5.0	5.0	
9-Dec-15	Rainy	Moderate	11:52	10.1	Surface	1.0	22.0 22.0	22.0	8.2 8.2	8.2	30.9 31.0	31.0	89.0 86.6	87.8	6.5 6.3	6.4	6.5	7.5 7.5	7.5	7.6	6.5 6.2	6.4	6.5
					Middle	5.1	22.0 22.0	22.0	8.2 8.2	8.2	31.0 30.9	31.0	87.7 90.2	89.0	6.4 6.6	6.5		7.6 7.7	7.7		6.5 7.2	6.9	
					Bottom	9.1	22.0 22.0	22.0	8.2 8.2	8.2	31.0 30.9	31.0	90.9 94.2	92.6	6.7 6.9	6.8		7.8 7.6	7.7		6.1 6.0	6.1	
11-Dec-15	Sunny	Moderate	12:50	10.5	Surface	1.0	21.7 21.7	21.7	8.2 8.2	8.2	31.0 31.0	31.0	85.5 85.4	85.5	6.3 6.3	6.3	6.3	11.0 11.0	11.0	11.8	6.0 5.3	5.7	6.9
					Middle	5.3	21.7 21.7	21.7	8.2 8.2	8.2	31.1 31.1	31.1	85.2 85.2	85.2	6.3 6.3	6.3		12.4 12.5	12.5		5.6 6.5	6.1	
					Bottom	9.5	21.7 21.7	21.7	8.2 8.2	8.2	31.1 31.1	31.1	85.9 85.3	85.6	6.3 6.3	6.3		12.1 11.8	12.0		8.4 9.5	9.0	
14-Dec-15	Rainy	Moderate	14:51	10.7	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	28.7 28.1	28.4	89.5 88.5	89.0	6.7 6.6	6.6	6.6	8.9 8.8	8.9	8.7	6.3 7.3	6.8	6.6
					Middle	5.4	21.7 21.7	21.7	8.2 8.2	8.2	29.5 29.4	29.4	88.4 89.9	89.2	6.6 6.7	6.6		8.6 8.6	8.6		5.4 6.4	5.9	
					Bottom	9.7	21.8 21.7	21.8	8.1 8.1	8.1	30.0 29.8	29.9	89.7 87.0	88.4	6.6 6.4	6.5		8.5 8.8	8.7		6.9 7.1	7.0	
16-Dec-15	Sunny	Moderate	16:31	10.8	Surface	1.0	21.2 21.1	21.2	8.2 8.2	8.2	28.3 28.4	28.4	86.2 86.5	86.4	6.5 6.5	6.5	6.5	4.7 5.0	4.9	4.8	8.3 8.0	8.2	8.3
					Middle	5.4	21.4 21.4	21.4	8.2 8.2	8.2	29.1 29.2	29.2	86.9 86.8	86.9	6.5 6.5	6.5		4.4 4.8	4.6		8.4 9.6	9.0	
					Bottom	9.8	21.4 21.4	21.4	8.2 8.1	8.2	29.3 29.2	29.3	88.0 88.7	88.4	6.6 6.6	6.6		5.0 4.5	4.8		7.8 7.6	7.7	
18-Dec-15	Sunny	Moderate	12:33	10.5	Surface	1.0	19.9 19.8	19.9	8.2 8.2	8.2	29.5 29.5	29.5	88.8 93.2	91.0	6.8 7.1	6.9	6.8	5.8 5.9	5.9	5.9	4.1 3.4	3.8	3.6
					Middle	5.3	20.1 20.2	20.1	8.2 8.2	8.2	30.4 30.5	30.4	88.8 88.2	88.5	6.7 6.7	6.7		5.9 5.9	5.9		3.2 3.6	3.4	
					Bottom	9.5	20.2 20.1	20.2	8.2 8.2	8.2	30.4 30.5	30.4	87.9 87.4	87.7	6.7 6.6	6.7		5.9 5.8	5.9		3.2 3.7	3.5	
21-Dec-15	Cloudy	Moderate	15:31	10.8	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.9 29.9	29.9	91.0 89.0	90.0	7.0 6.8	6.9	6.8	3.4 3.6	3.5	3.6	5.2 4.4	4.8	6.6
					Middle	5.4	19.7 19.7	19.7	8.2 8.2	8.2	30.3 30.3	30.3	86.3 87.4	86.9	6.6 6.7	6.6		3.7 3.6	3.7		4.3 5.4	4.9	
					Bottom	9.8	19.7 19.8	19.7	8.2 8.2	8.2	30.3 30.4	30.4	87.7 87.0	87.4	6.7 6.6	6.7		3.6 3.8	3.7		10.2 10.1	10.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	11:10	10.2	Surface	1.0	19.8 19.8	19.8	8.2 8.2	8.2	28.6 28.8	28.7	91.2 91.4	91.3	7.0 7.0	7.0	7.0	5.7 5.7	5.7	6.1	4.1 5.5	4.8	5.6
					Middle	5.1	19.8 19.8	19.8	8.2 8.2	8.2	29.8 29.9	29.9	89.3 90.0	89.7	6.8 6.9	6.9		6.1 6.4	6.3		5.2 4.4	4.8	
					Bottom	9.2	19.8 19.8	19.8	8.2 8.2	8.2	29.9 29.9	29.9	88.8 88.6	88.7	6.8 6.8	6.8		6.2 6.3	6.3		6.7 7.9	7.3	
25-Dec-15	Cloudy	Moderate	12:43	10.3	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	27.2 27.3	27.2	88.8 89.1	89.0	6.9 6.9	6.9	7.0	7.4 7.3	7.4	7.4	5.9 6.3	6.1	6.1
					Middle	5.2	20.4 20.4	20.4	8.1 8.1	8.1	28.5 28.7	28.6	93.4 89.6	91.5	7.1 6.8	7.0		7.5 7.3	7.4		6.1 6.4	6.3	
					Bottom	9.3	20.1 20.4	20.3	8.2 8.1	8.1	28.9 28.8	28.8	89.6 89.9	89.8	6.9 6.8	6.8		7.3 7.5	7.4		5.8 5.7	5.8	
28-Dec-15	Sunny	Moderate	14:36	10.1	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	28.2 28.2	28.2	91.2 89.9	90.6	7.1 7.0	7.0	6.9	6.1 6.4	6.3	6.3	9.7 9.3	9.5	9.0
					Middle	5.1	19.6 19.6	19.6	8.2 8.2	8.2	28.6 28.6	28.6	87.6 88.4	88.0	6.8 6.8	6.8		6.1 6.3	6.2		9.2 8.7	9.0	
					Bottom	9.1	19.7 19.7	19.7	8.2 8.2	8.2	28.8 28.8	28.8	88.7 86.9	87.8	6.8 6.7	6.8		6.2 6.3	6.3		8.9 7.8	8.4	
30-Dec-15	Cloudy	Moderate	15:55	10.6	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	29.0 29.0	29.0	89.3 88.5	88.9	6.9 6.9	6.9	6.9	7.3 7.0	7.2	6.7	9.2 9.7	9.5	10.3
					Middle	5.3	19.6 19.6	19.6	8.2 8.2	8.2	29.2 29.2	29.2	90.4 89.6	90.0	7.0 6.9	6.9		6.0 6.0	6.0		10.9 10.3	10.6	
					Bottom	9.6	19.6 19.6	19.6	8.2 8.2	8.2	29.3 29.3	29.3	87.8 88.1	88.0	6.8 6.8	6.8		6.8 7.0	6.9		11.2 10.3	10.8	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	12:15	10.1	Surface	1.0	23.7 23.8	23.7	8.1 8.1	8.1	25.2 25.2	25.2	88.4 90.7	89.6	6.5 6.6	6.6	6.5	4.6 4.7	4.7	5.0	4.2 3.3	3.8	3.5
					Middle	5.1	23.6 23.6	23.6	8.1 8.1	8.1	26.0 26.0	26.0	88.3 86.6	87.5	6.5 6.3	6.4		5.1 5.1	5.1		3.5 3.1	3.3	
					Bottom	9.1	23.6 23.7	23.6	8.1 8.1	8.1	27.2 27.2	27.2	87.6 86.9	87.3	6.4 6.3	6.3		5.1 5.2	5.2		3.3 3.4	3.4	
4-Dec-15	Cloudy	Moderate	14:03	10.5	Surface	1.0	22.9 23.0	23.0	8.1 8.1	8.1	26.6 26.5	26.5	87.9 87.3	87.6	6.5 6.4	6.5	6.5	3.1 3.1	3.1	3.2	4.4 4.5	4.5	5.1
					Middle	5.3	23.6 23.3	23.4	8.1 8.1	8.1	28.1 28.0	28.1	87.9 88.7	88.3	6.4 6.4	6.4		3.2 3.1	3.2		5.3 4.9	5.1	
					Bottom	9.5	23.3 23.5	23.4	8.1 8.1	8.1	30.7 30.5	30.6	88.0 91.3	89.7	6.3 6.5	6.4		3.3 3.0	3.2		5.3 6.2	5.8	
7-Dec-15	Cloudy	Moderate	16:08	10.2	Surface	1.0	22.7 22.7	22.7	8.2 8.2	8.2	30.3 30.5	30.4	91.2 86.6	88.9	6.5 6.2	6.4	6.4	4.6 4.7	4.7	5.1	5.7 5.9	5.8	5.7
					Middle	5.1	22.9 22.9	22.9	8.2 8.2	8.2	31.6 31.5	31.5	85.8 89.0	87.4	6.2 6.4	6.3		5.2 5.1	5.2		5.2 6.2	5.7	
					Bottom	9.2	22.9 22.8	22.9	8.2 8.2	8.2	31.5 31.6	31.5	88.7 85.5	87.1	6.4 6.1	6.3		5.3 5.4	5.4		5.3 5.8	5.6	
9-Dec-15	Rainy	Moderate	16:56	10.6	Surface	1.0	22.0 22.0	22.0	8.2 8.2	8.2	30.7 30.7	30.7	88.0 86.4	87.2	6.4 6.3	6.4	6.4	6.0 5.7	5.9	5.8	7.4 7.0	7.2	7.2
					Middle	5.3	22.0 22.0	22.0	8.2 8.2	8.2	30.8 30.7	30.8	86.5 85.5	86.0	6.3 6.3	6.3		5.6 6.0	5.8		7.2 6.9	7.1	
					Bottom	9.6	22.0 22.0	22.0	8.2 8.2	8.2	30.8 30.7	30.8	86.0 85.9	86.0	6.3 6.3	6.3		5.6 5.8	5.7		7.5 6.9	7.2	
11-Dec-15	Sunny	Moderate	07:17	10.8	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.6	30.7	91.1 90.4	90.8	6.7 6.7	6.7	6.7	11.3 10.0	10.7	10.7	11.0 11.2	11.1	10.6
					Middle	5.4	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.6	30.6	88.6 91.5	90.1	6.5 6.8	6.6		10.9 10.3	10.6		11.0 11.0	11.0	
					Bottom	9.8	21.6 21.6	21.6	8.2 8.2	8.2	30.7 30.6	30.6	88.5 94.7	91.6	6.5 7.0	6.8		11.5 10.3	10.9		9.6 9.8	9.7	
14-Dec-15	Rainy	Moderate	09:46	10.0	Surface	1.0	21.6 21.6	21.6	8.1 8.1	8.1	28.5 28.4	28.5	89.7 91.7	90.7	6.7 6.8	6.8	6.8	8.2 8.0	8.1	12.1	8.5 8.7	8.6	8.8
					Middle	5.0	21.6 21.6	21.6	8.1 8.1	8.1	28.8 28.9	28.8	90.6 89.1	89.9	6.8 6.6	6.7		14.5 13.4	14.0		8.0 9.0	8.5	
					Bottom	9.0	21.6 21.6	21.6	8.1 8.1	8.1	29.2 29.2	29.2	87.6 88.7	88.2	6.5 6.6	6.6		13.9 14.5	14.2		9.4 9.3	9.4	
16-Dec-15	Sunny	Moderate	11:06	10.5	Surface	1.0	20.9 20.8	20.9	8.1 8.2	8.1	27.9 28.0	28.0	92.7 87.9	90.3	7.0 6.7	6.9	6.9	8.5 8.3	8.4	8.6	8.1 8.2	8.2	7.8
					Middle	5.3	21.2 21.2	21.2	8.1 8.1	8.1	28.4 28.5	28.4	93.8 89.7	91.8	7.1 6.7	6.9		7.8 8.0	7.9		7.3 7.0	7.2	
					Bottom	9.5	21.2 21.2	21.2	8.1 8.1	8.1	28.4 28.3	28.4	88.9 96.7	92.8	6.7 7.3	7.0		9.8 9.3	9.6		8.0 7.9	8.0	
18-Dec-15	Cloudy	Moderate	05:26	10.7	Surface	1.0	19.3 18.7	19.0	8.2 8.2	8.2	28.4 28.3	28.3	91.0 100.8	95.9	7.1 7.6	7.3	7.2	6.8 6.8	6.8	6.8	3.7 3.7	3.7	3.6
					Middle	5.4	20.1 20.0	20.1	8.2 8.2	8.2	30.0 30.0	30.0	94.9 90.6	92.8	7.3 6.9	7.1		6.8 6.7	6.8		3.6 3.6	3.6	
					Bottom	9.7	20.1 20.5	20.3	8.2 8.1	8.1	30.4 30.2	30.3	90.4 92.6	91.5	6.9 7.2	7.1		6.8 6.8	6.8		3.7 3.0	3.4	
21-Dec-15	Sunny	Moderate	08:58	10.8	Surface	1.0	20.0 20.0	20.0	8.2 8.2	8.2	30.8 30.8	30.8	89.5 85.1	87.3	6.8 6.5	6.6	6.5	2.8 2.9	2.9	2.9	3.2 4.6	3.9	4.2
					Middle	5.4	20.1 20.2	20.2	8.2 8.2	8.2	30.9 31.0	31.0	85.2 84.8	85.0	6.4 6.4	6.4		2.7 2.9	2.8		5.0 3.3	4.2	
					Bottom	9.8	20.1 20.2	20.2	8.2 8.2	8.2	30.9 31.0	31.0	85.1 85.2	85.2	6.4 6.4	6.4		2.9 3.0	3.0		5.0 4.0	4.5	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	16:41	10.4	Surface	1.0	19.9 19.9	19.9	8.2 8.2	8.2	29.0 29.0	29.0	88.4 87.9	88.2	6.8 6.7	6.8	6.8	7.6 7.5	7.6	7.5	4.3 2.9	3.6	3.4
					Middle	5.2	20.0 20.0	20.0	8.2 8.2	8.2	30.3 30.2	30.2	88.2 87.9	88.1	6.7 6.7	6.7		7.4 7.6	7.5		3.5 3.2	3.4	
					Bottom	9.4	20.0 19.9	20.0	8.2 8.2	8.2	30.5 30.4	30.5	88.4 88.6	88.5	6.7 6.7	6.7		7.7 7.3	7.5		3.1 3.5	3.3	
25-Dec-15	Cloudy	Moderate	07:42	10.2	Surface	1.0	20.1 20.1	20.1	8.1 8.1	8.1	27.1 27.1	27.1	91.3 90.8	91.1	7.1 7.0	7.0	7.0	8.7 8.5	8.6	8.7	5.5 6.1	5.8	6.1
					Middle	5.1	20.2 20.2	20.2	8.1 8.1	8.1	27.3 27.4	27.4	87.9 91.7	89.8	6.8 7.1	6.9		8.6 8.7	8.7		6.2 7.1	6.7	
					Bottom	9.2	20.2 20.2	20.2	8.1 8.1	8.1	28.3 28.4	28.3	95.4 89.2	92.3	7.3 6.8	7.1		8.7 8.6	8.7		5.8 5.9	5.9	
28-Dec-15	Sunny	Moderate	09:18	11.1	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	27.9 27.9	27.9	88.9 88.6	88.8	6.9 6.9	6.9	6.9	8.8 8.8	8.8	9.5	7.7 8.4	8.1	8.8
					Middle	5.6	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	89.2 88.0	88.6	7.0 6.9	6.9		9.9 9.7	9.8		8.7 8.7	8.7	
					Bottom	10.1	19.4 19.4	19.4	8.1 8.2	8.2	28.0 28.0	28.0	91.1 88.7	89.9	7.1 6.9	7.0		9.8 9.9	9.9		9.7 9.2	9.5	
30-Dec-15	Cloudy	Moderate	10:48	10.8	Surface	1.0	19.5 19.6	19.6	8.2 8.2	8.2	28.6 28.7	28.6	87.1 86.5	86.8	6.8 6.7	6.7	6.7	4.8 5.0	4.9	6.8	5.8 4.2	5.0	4.3
					Middle	5.4	19.7 19.7	19.7	8.2 8.2	8.2	29.2 29.3	29.3	84.8 86.3	85.6	6.5 6.6	6.6		6.9 7.2	7.1		4.3 4.5	4.4	
					Bottom	9.8	19.7 19.7	19.7	8.1 8.1	8.1	29.3 29.3	29.3	85.0 86.6	85.8	6.5 6.7	6.6		8.8 8.0	8.4		3.1 4.1	3.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
2-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	23.9 23.9	23.9	8.0 8.0	8.0	25.7 26.1	25.9	90.7 90.2	90.5	6.6 6.6	6.6	6.6	6.6	7.6 7.3	7.5	7.5	9.3 8.6	9.0	9.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
4-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	22.9 23.0	22.9	8.1 8.1	8.1	25.9 26.2	26.1	84.7 85.1	84.9	6.3 6.3	6.3	6.3	6.3	5.8 5.8	5.8	5.8	3.9 2.1	3.0	3.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	22.0 22.0	22.0	8.2 8.2	8.2	29.0 29.1	29.1	85.3 85.0	85.2	6.3 6.3	6.3	6.3	6.3	6.4 6.6	6.5	6.5	6.4 6.7	6.6	6.6
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
9-Dec-15	Rainy	Moderate	-	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.6	21.4 21.4	21.4	8.2 8.2	8.2	30.2 30.2	30.2	85.0 85.1	85.1	6.3 6.3	6.3	6.3	9.8 9.8	9.8	9.8	10.7 10.0	10.4	10.4	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
11-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	21.5 21.4	21.5	8.2 8.3	8.3	30.4 30.4	30.4	87.3 89.8	88.6	6.5 6.7	6.6	6.6	8.0 8.3	8.2	8.2	10.7 11.6	11.2	11.2	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14-Dec-15	Rainy	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.1	30.1	90.0 90.6	90.3	6.7 6.7	6.7	6.7	10.4 10.5	10.5	10.5	13.0 14.2	13.6	13.6	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
16-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	20.3 20.3	20.3	8.3 8.3	8.3	25.7 25.6	25.6	94.6 96.0	95.3	7.4 7.5	7.4	7.4	9.7 9.3	9.5	9.5	10.8 10.9	10.9	10.9	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
18-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	18.9 18.9	18.9	8.3 8.3	8.3	28.7 28.7	28.7	95.0 91.8	93.4	7.5 7.2	7.3	7.3	5.8 5.9	5.9	5.9	9.9 9.4	9.7	9.7	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21-Dec-15	Cloudy	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	19.3 19.3	19.3	8.4 8.4	8.4	28.9 29.0	28.9	90.1 89.6	89.9	7.0 7.0	7.0	7.0	3.7 3.8	3.8	3.8	6.7 6.7	6.7	6.7	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
					Middle	0.7	19.7	19.7	8.2	8.2	29.6	29.6	89.8	90.7	6.9	7.0	7.0	7.8	7.8	7.8	12.1	11.3	11.3
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
					Middle	0.7	20.3	20.3	8.2	8.2	28.5	28.5	92.8	92.4	7.1	7.1	7.1	3.8	3.8	3.8	4.1	4.3	4.3
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
28-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
					Middle	0.7	19.3	19.3	8.3	8.3	28.2	28.2	90.5	89.8	7.1	7.0	7.0	7.8	7.7	7.7	9.0	8.8	8.8
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30-Dec-15	Cloudy	Moderate	-	1.8	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
					Middle	0.9	19.3	19.3	8.2	8.2	28.6	28.7	96.4	94.6	7.5	7.4	7.4	9.5	10.0	10.0	11.1	11.8	11.8
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

CS4 and CS(Mf)3 are considered as upstream control stations of mid-ebb tide. The averaged turbidity and suspended solid values of these stations will be used for determination of Action and Limit Levels.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
2-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	23.9 23.9	23.9	8.1 8.1	8.1	25.6 25.6	25.6	89.1 89.0	89.1	6.5 6.5	6.5	6.5	6.5	6.5	9.5 9.6	9.6	9.6	9.2 7.8	8.5	8.5
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
4-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	22.6 22.6	22.6	8.3 8.2	8.3	26.7 26.7	26.7	92.4 90.8	91.6	6.9 6.7	6.8	6.8	6.8	4.8 4.8	4.8	4.8	4.4 4.8	4.6	4.6	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	22.3 22.4	22.4	8.2 8.2	8.2	30.3 30.3	30.3	88.2 93.7	91.0	6.4 6.8	6.6	6.6	6.6	4.6 4.6	4.6	4.6	7.1 7.4	7.3	7.3	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
9-Dec-15	Rainy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	21.4 21.3	21.4	8.0 8.0	8.0	28.0 27.9	28.0	88.2 86.7	87.5	6.6 6.5	6.6	6.6	6.6	6.8 6.7	6.8	6.8	6.2 6.7	6.5	6.5	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
11-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	21.4 21.3	21.4	8.2 8.2	8.2	30.4 30.4	30.4	83.7 83.9	83.8	6.2 6.2	6.2	6.2	6.2	6.6 6.5	6.6	6.6	8.8 8.1	8.5	8.5	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14-Dec-15	Rainy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	21.6 21.6	21.6	8.2 8.2	8.2	30.1 30.1	30.1	89.5 89.2	89.4	6.6 6.6	6.6	6.6	6.6	8.5 8.6	8.6	8.6	12.4 10.1	11.3	11.3	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
16-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	20.3 20.3	20.3	8.1 8.1	8.1	27.4 27.4	27.4	87.5 87.7	87.6	6.7 6.8	6.7	6.7	6.7	12.5 11.9	12.2	12.2	19.3 18.9	19.1	19.1	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
18-Dec-15	Cloudy	Moderate	-	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.6	18.8 18.8	18.8	8.2 8.2	8.2	28.3 28.4	28.3	95.5 97.8	96.7	7.5 7.7	7.6	7.6	7.6	8.1 8.1	8.1	8.1	5.3 6.2	5.8	5.8	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	18.8 18.8	18.8	8.2 8.2	8.2	30.4 30.4	30.4	87.0 87.1	87.1	6.8 6.8	6.8	6.8	6.8	5.1 4.7	4.9	4.9	7.3 6.2	6.8	6.8	
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-Dec-15	Sunny	Moderate	-	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	<u>19.9</u> <u>19.9</u>	19.9	<u>8.4</u> <u>8.4</u>	8.4	30.0 30.0	30.0	<u>91.0</u> <u>89.0</u>	90.0	<u>7.0</u> <u>6.8</u>	6.9	6.9	6.5 6.4	6.5	6.5	6.5	7.8 8.1	8.0	8.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25-Dec-15	Cloudy	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	<u>20.3</u> <u>20.3</u>	20.3	<u>8.2</u> <u>8.2</u>	8.2	28.5 28.5	28.5	<u>90.7</u> <u>90.9</u>	90.8	<u>6.9</u> <u>7.0</u>	6.9	6.9	4.4 4.5	4.5	4.5	4.5	4.8 5.3	5.1	5.1
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
28-Dec-15	Sunny	Moderate	-	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	<u>19.2</u> <u>19.3</u>	19.3	<u>8.2</u> <u>8.2</u>	8.2	27.9 27.9	27.9	<u>92.7</u> <u>90.4</u>	91.6	<u>7.3</u> <u>7.1</u>	7.2	7.2	10.5 10.5	10.5	10.5	10.5	11.7 14.1	12.9	12.9
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30-Dec-15	Cloudy	Moderate	-	1.8	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.9	<u>19.2</u> <u>19.2</u>	19.2	<u>8.2</u> <u>8.2</u>	8.2	28.2 28.2	28.2	<u>88.9</u> <u>88.9</u>	88.9	<u>6.9</u> <u>7.0</u>	6.9	6.9	6.8 6.8	6.8	6.8	6.8	8.4 8.9	8.7	8.7
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

CS6, CSA and CS(Mf)5 are considered as upstream control stations of mid-flood tide. The averaged turbidity and suspended solid values of these stations will be used for determination of Action and Limit Levels.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	17:25	3.7	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	27.3 27.3	27.3	90.4 90.2	90.3	6.5 6.5	6.5	6.5	7.4 7.1	7.3	7.4	7.8 7.1	7.5	7.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	23.8 23.9	23.9	8.1 8.1	8.1	27.4 27.4	27.4	91.3 90.2	90.8	6.6 6.5	6.6		7.3 7.4	7.4		6.6	6.6		7.3 7.4	7.4	6.6
4-Dec-15	Cloudy	Moderate	06:51	3.7	Surface	1.0	22.9 23.0	22.9	8.1 8.1	8.1	24.8 24.8	24.8	82.3 82.1	82.2	6.1 6.1	6.1	6.1	6.3 6.6	6.5	6.6	2.6 4.1	3.4	3.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	23.6 23.0	23.3	8.1 8.1	8.1	26.8 28.1	27.5	83.2 84.8	84.0	6.0 6.2	6.1		6.1	6.1		6.1	6.1		6.5 6.6	6.6	6.1
7-Dec-15	Cloudy	Moderate	10:42	3.7	Surface	1.0	22.0 22.1	22.1	8.1 8.1	8.1	28.7 28.6	28.7	82.8 84.0	83.4	6.1 6.2	6.2	6.2	5.2 5.0	5.1	5.2	3.2 4.1	3.7	4.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	22.2 22.7	22.4	8.1 8.1	8.1	29.5 29.3	29.4	83.5 85.3	84.4	6.1 6.2	6.2		6.2	6.2		6.2	6.2		5.1 5.2	5.2	6.2
9-Dec-15	Rainy	Moderate	12:14	3.8	Surface	1.0	21.6 21.7	21.6	8.2 8.2	8.2	30.0 30.0	30.0	87.0 85.9	86.5	6.4 6.4	6.4	6.4	3.1 3.2	3.2	3.2	4.5 3.4	4.0	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.8	21.6 22.1	21.9	8.2 8.2	8.2	30.1 30.1	30.1	86.4 86.2	86.3	6.4 6.3	6.4		6.4	6.4		6.4	6.4		3.1 3.2	3.2	6.4
11-Dec-15	Sunny	Moderate	12:19	3.7	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	30.8 30.8	30.8	88.7 87.5	88.1	6.5 6.4	6.5	6.5	6.2 5.8	6.0	5.9	7.6 7.0	7.3	7.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	21.6 21.6	21.6	8.2 8.2	8.2	30.9 30.9	30.9	90.2 88.2	89.2	6.6 6.5	6.6		6.6	6.6		6.6	6.6		5.8 5.8	5.8	6.6
14-Dec-15	Rainy	Moderate	14:28	3.7	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	28.3 28.3	28.3	92.7 93.4	93.1	6.9 7.0	7.0	7.0	6.5 6.3	6.4	6.5	4.1 5.2	4.7	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	21.5 21.5	21.5	8.2 8.1	8.2	29.4 29.4	29.4	93.5 94.7	94.1	7.0 7.0	7.0		7.0	7.0		7.0	7.0		6.5 6.6	6.6	7.0
16-Dec-15	Sunny	Moderate	16:01	3.6	Surface	1.0	20.7 20.6	20.6	8.2 8.1	8.2	26.8 26.8	26.8	91.5 92.9	92.2	7.0 7.1	7.1	7.1	8.3 8.2	8.3	8.2	8.4 8.6	8.5	8.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.6	20.7 20.7	20.7	8.1 8.1	8.1	27.1 27.2	27.1	99.1 91.8	95.5	7.6 7.0	7.3		7.3	7.3		7.3	7.3		8.0 8.1	8.1	7.3
18-Dec-15	Sunny	Moderate	12:14	3.7	Surface	1.0	19.4 19.7	19.5	8.2 8.2	8.2	28.8 29.4	29.1	90.4 90.0	90.2	7.0 6.9	7.0	7.0	8.5 8.5	8.5	8.5	3.7 3.8	3.8	3.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	19.9 19.5	19.7	8.2 8.2	8.2	29.6 30.0	29.8	94.1 90.8	92.5	7.2 7.0	7.1		7.1	7.1		7.1	7.1		8.5 8.4	8.5	7.1
21-Dec-15	Cloudy	Moderate	14:49	3.6	Surface	1.0	19.8 19.8	19.8	8.2 8.2	8.2	29.9 29.9	29.9	88.2 89.3	88.8	6.8 6.8	6.8	6.8	7.2 7.2	7.2	7.2	8.9 7.7	8.3	8.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.6	19.7 19.8	19.7	8.2 8.2	8.2	30.0 29.9	30.0	90.4 88.2	89.3	6.9 6.8	6.8		6.8	6.8		6.8	6.8		7.0 7.2	7.1	6.8

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	11:36	4.0	Surface	1.0	20.2 20.2	20.2	8.1 8.1	8.1	30.1 30.1	30.1	91.6 91.9	91.8	7.0 7.0	7.0	7.0	5.6 5.6	5.6	5.6	8.3 8.3	8.3	8.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.0	20.1 20.1	20.1	8.2 8.1	8.2	30.2 30.2	30.2	90.4 89.6	90.0	6.9 6.8	6.8		5.5 5.7	5.6		6.9 8.6	7.8				
25-Dec-15	Cloudy	Moderate	12:23	3.7	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	27.2 26.9	27.1	92.6 93.0	92.8	7.2 7.2	7.2	7.2	5.5 5.5	5.5	5.6	5.0 5.0	5.0	5.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.7	20.2 20.1	20.2	8.1 8.2	8.2	28.0 27.4	27.7	93.0 93.6	93.3	7.1 7.2	7.2		5.5 5.6	5.6		5.7 5.7	5.7				
28-Dec-15	Sunny	Moderate	14:16	3.8	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	92.3 89.2	90.8	7.2 6.9	7.1	7.1	8.8 8.8	8.8	8.8	9.5 8.3	8.9	9.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	19.4 19.4	19.4	8.2 8.2	8.2	28.0 28.0	28.0	94.3 91.1	92.7	7.4 7.1	7.2		8.9 8.7	8.8		9.9 10.6	10.3				
30-Dec-15	Cloudy	Moderate	15:22	3.8	Surface	1.0	19.5 19.4	19.4	8.2 8.2	8.2	28.6 28.6	28.6	91.4 91.7	91.6	7.1 7.1	7.1	7.1	5.7 5.6	5.7	5.8	5.4 5.4	5.4	5.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	19.5 19.5	19.5	8.2 8.2	8.2	28.7 28.8	28.7	90.7 94.4	92.6	7.0 7.3	7.2		5.6 6.0	5.8		5.6 5.6	5.6				

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	12:37	3.7	Surface	1.0	23.7 23.7	23.7	8.1 8.1	8.1	25.5 25.5	25.5	87.9 89.2	88.6	6.4 6.5	6.5	6.5	8.3 8.5	8.4	8.5	6.9 6.7	6.8	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	23.6 23.7	23.6	8.1 8.1	8.1	25.8 25.6	25.7	89.5 88.1	88.8	6.5 6.5	6.5		8.5 8.7	8.6		6.5	8.5 8.7		8.6	6.5	6.1 6.3	6.2
4-Dec-15	Cloudy	Moderate	13:40	3.8	Surface	1.0	23.0 23.0	23.0	8.1 8.1	8.1	26.9 26.9	26.9	87.5 90.6	89.1	6.4 6.7	6.5	6.5	12.5 12.4	12.5	12.5	5.2 4.5	4.9	7.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	23.0 23.0	23.0	8.1 8.1	8.1	27.0 27.1	27.0	93.7 88.6	91.2	6.9 6.5	6.7		12.5 12.4	12.5		6.7	12.5 12.4		12.5	6.7	9.9 10.1	10.0
7-Dec-15	Cloudy	Moderate	15:46	3.7	Surface	1.0	22.0 22.1	22.0	8.2 8.2	8.2	29.6 29.7	29.6	89.0 91.2	90.1	6.6 6.7	6.6	6.6	6.7 6.6	6.7	6.7	5.0 5.0	5.0	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	22.1 22.3	22.2	8.2 8.2	8.2	29.9 30.1	30.0	89.8 94.7	92.3	6.6 6.9	6.8		6.8 6.6	6.7		6.8	6.8 6.6		6.7	6.8	5.1 4.2	4.7
9-Dec-15	Rainy	Moderate	16:33	3.7	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	29.5 29.5	29.5	88.9 87.7	88.3	6.6 6.5	6.6	6.6	10.2 10.0	10.1	10.2	5.0 4.6	4.8	5.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	21.6 21.7	21.7	8.2 8.2	8.2	29.6 29.6	29.6	88.6 92.3	90.5	6.6 6.8	6.7		10.2 10.2	10.2		6.7	10.2 10.2		10.2	6.7	5.8 6.1	6.0
11-Dec-15	Sunny	Moderate	07:52	3.9	Surface	1.0	21.5 21.5	21.5	8.2 8.2	8.2	30.8 30.8	30.8	85.4 84.9	85.2	6.3 6.3	6.3	6.3	6.0 6.0	6.0	6.1	4.8 5.2	5.0	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	21.5 21.6	21.6	8.2 8.2	8.2	30.8 30.8	30.8	85.0 85.0	85.0	6.3 6.3	6.3		6.1 6.2	6.2		6.3	6.1 6.2		6.2	6.3	4.9 4.7	4.8
14-Dec-15	Rainy	Moderate	10:11	3.8	Surface	1.0	21.5 21.5	21.5	8.1 8.1	8.1	28.4 28.4	28.4	87.5 87.8	87.7	6.6 6.6	6.6	6.6	11.2 11.4	11.3	11.2	10.0 11.2	10.6	11.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	21.5 21.5	21.5	8.1 8.1	8.1	28.5 28.5	28.5	87.5 87.4	87.5	6.6 6.5	6.5		11.1 11.0	11.1		6.5	11.1 11.0		11.1	6.5	11.1 12.5	11.8
16-Dec-15	Sunny	Moderate	11:44	3.7	Surface	1.0	20.5 20.5	20.5	8.1 8.1	8.1	27.4 27.4	27.4	86.9 87.5	87.2	6.7 6.7	6.7	6.7	6.6 6.0	6.3	7.3	9.4 8.6	9.0	8.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	20.5 20.5	20.5	8.1 8.1	8.1	27.5 27.5	27.5	87.4 87.4	87.4	6.7 6.7	6.7		8.1 8.3	8.2		6.7	8.1 8.3		8.2	6.7	7.7 8.5	8.1
18-Dec-15	Cloudy	Moderate	05:46	3.7	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	28.8 28.6	28.7	86.7 87.4	87.1	6.7 6.8	6.7	6.7	4.4 4.3	4.4	4.4	3.7 4.4	4.1	3.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	20.1 19.8	20.0	8.2 8.2	8.2	29.7 29.9	29.8	87.8 87.7	87.8	6.7 6.7	6.7		4.4 4.2	4.3		6.7	4.4 4.2		4.3	6.7	3.2 3.9	3.6
21-Dec-15	Sunny	Moderate	09:34	3.8	Surface	1.0	19.6 19.5	19.5	8.2 8.2	8.2	30.3 30.3	30.3	84.9 84.9	84.9	6.5 6.5	6.5	6.5	3.6 4.0	3.8	3.7	11.2 11.1	11.2	11.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	19.7 19.5	19.6	8.2 8.2	8.2	30.5 30.4	30.5	85.1 85.3	85.2	6.5 6.5	6.5		3.7 3.3	3.5		6.5	3.7 3.3		3.5	6.5	12.0 10.9	11.5

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	16:21	3.7	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	29.9 29.8	29.8	91.0 90.9	91.0	6.9 6.9	6.9	6.9	8.4 8.6	8.5	8.5	10.2 11.7	11.0	10.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	20.3 20.3	20.3	8.2 8.2	8.2	30.0 30.4	30.2	91.0 91.3	91.2	6.9 6.9	6.9		8.4 8.6	8.5		9.5 11.0	10.3				
25-Dec-15	Cloudy	Moderate	08:03	3.6	Surface	1.0	20.0 20.1	20.1	8.1 8.1	8.1	27.0 27.1	27.0	89.9 92.4	91.2	7.0 7.2	7.1	7.1	6.4 6.6	6.5	6.6	7.7 6.2	7.0	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	20.1 20.1	20.1	8.1 8.1	8.1	27.1 27.3	27.2	88.8 88.7	88.8	6.9 6.9	6.9		6.5 6.6	6.6		8.0 8.3	8.2				
28-Dec-15	Sunny	Moderate	09:37	3.7	Surface	1.0	19.4 19.4	19.4	8.1 8.1	8.1	27.9 27.9	27.9	87.1 87.2	87.2	6.8 6.8	6.8	6.8	8.9 8.7	8.8	8.9	6.2 6.3	6.3	6.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.7	19.4 19.4	19.4	8.1 8.1	8.1	28.0 28.0	28.0	87.1 87.3	87.2	6.8 6.8	6.8		8.9 8.9	8.9		7.2 7.1	7.2				
30-Dec-15	Cloudy	Moderate	11:23	3.8	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	28.4 28.4	28.4	88.7 86.8	87.8	6.9 6.8	6.8	6.8	14.7 14.6	14.7	14.9	21.0 19.1	20.1	18.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.8	19.4 19.4	19.4	8.2 8.2	8.2	28.5 28.6	28.5	87.1 86.8	87.0	6.8 6.7	6.8		14.8 15.2	15.0		16.2 16.5	16.4				

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	17:11	4.9	Surface	1.0	20.3 20.4	20.3	8.2 8.2	8.2	24.9 24.2	24.5	94.2 95.6	94.9	7.4 7.4	7.4	7.4	4.3 4.2	4.3	4.4	4.0 3.6	3.8	3.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.9	20.3 20.4	20.4	8.1 8.1	8.1	26.9 28.0	27.4	94.1 93.5	93.8	7.3 7.3	7.3		7.3	4.4 4.4		4.4	7.3		4.4 4.4	4.4	4.2 3.3
4-Dec-15	Cloudy	Moderate	06:14	5.0	Surface	1.0	19.3 19.2	19.2	8.1 8.1	8.1	28.2 28.2	28.2	93.9 94.5	94.2	7.3 7.4	7.3	7.3	2.7 2.7	2.7	2.8	3.4 4.0	3.7	3.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	19.3 19.3	19.3	8.1 8.1	8.1	28.6 28.2	28.4	92.4 92.3	92.4	7.3 7.3	7.3		7.3	2.8 2.8		2.8	7.3		2.8 2.8	2.8	3.1 3.5
7-Dec-15	Cloudy	Moderate	10:48	4.0	Surface	1.0	19.3 19.2	19.3	8.2 8.2	8.2	34.3 34.6	34.4	93.7 93.0	93.4	7.0 7.0	7.0	7.0	5.5 5.4	5.5	5.6	6.0 6.6	6.3	6.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.0	19.3 19.2	19.3	8.2 8.2	8.2	34.6 35.0	34.8	92.4 92.1	92.3	7.0 7.0	7.0		7.0	5.6 5.6		5.6	7.0		5.6 5.6	5.6	5.3 6.0
9-Dec-15	Rainy	Moderate	11:27	5.0	Surface	1.0	18.5 18.5	18.5	8.2 8.2	8.2	34.1 33.9	34.0	93.4 93.2	93.3	7.1 7.1	7.1	7.1	4.4 4.2	4.3	4.4	2.7 2.8	2.8	3.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	18.5 18.5	18.5	8.2 8.2	8.2	34.0 34.1	34.1	92.1 92.1	92.1	7.1 7.0	7.1		7.1	4.5 4.5		4.5	7.1		4.5 3.7	4.5	2.7 3.7
11-Dec-15	Sunny	Moderate	12:35	4.9	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	28.6 28.7	28.6	95.6 95.8	95.7	7.6 7.6	7.6	7.6	5.6 5.5	5.6	5.7	5.9 5.0	5.5	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.9	18.2 18.2	18.2	8.2 8.2	8.2	29.7 30.8	30.2	95.9 96.9	96.4	7.6 7.6	7.6		7.6	5.7 5.6		5.7	7.6		5.7 5.6	5.7	5.3 5.8
14-Dec-15	Rainy	Moderate	14:28	4.9	Surface	1.0	17.8 17.8	17.8	8.1 8.1	8.1	20.2 20.3	20.3	92.1 93.2	92.7	7.8 7.7	7.7	7.7	5.4 5.5	5.5	5.7	4.5 4.4	4.5	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.9	17.9 18.0	17.9	8.1 8.0	8.1	22.4 27.0	24.7	91.2 92.3	91.8	7.7 7.6	7.6		7.6	5.8 5.9		5.9	7.6		5.8 5.9	5.9	5.6 5.7
16-Dec-15	Sunny	Moderate	16:22	5.0	Surface	1.0	17.5 17.5	17.5	8.2 8.2	8.2	27.5 27.9	27.7	92.9 94.3	93.6	7.5 7.6	7.6	7.6	6.3 6.4	6.4	6.4	9.0 9.9	9.5	9.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	17.5 17.6	17.6	8.2 8.2	8.2	27.7 29.3	28.5	97.4 94.0	95.7	7.8 7.6	7.7		7.7	6.4 6.4		6.4	7.7		6.4 6.4	6.4	9.8 9.2
18-Dec-15	Sunny	Moderate	12:40	5.2	Surface	1.0	16.6 16.6	16.6	8.1 8.1	8.1	30.7 31.9	31.3	96.5 95.6	96.1	7.8 7.7	7.8	7.8	8.5 8.5	8.5	8.6	9.7 8.8	9.3	9.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.2	16.6 16.6	16.6	8.1 8.1	8.1	30.8 32.6	31.7	102.0 106.1	104.1	8.2 8.5	8.3		8.3	8.4 8.9		8.7	8.3		8.4 8.9	8.7	8.7 8.7
21-Dec-15	Cloudy	Moderate	09:17	5.0	Surface	1.0	15.7 15.6	15.6	8.1 8.1	8.1	30.8 30.6	30.7	95.4 96.0	95.7	7.9 7.9	7.9	7.9	2.8 2.8	2.8	2.8	3.3 2.4	2.9	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	15.6 15.8	15.7	8.1 8.1	8.1	30.8 30.8	30.8	95.6 95.5	95.6	7.9 7.8	7.9		7.9	2.8 2.8		2.8	7.9		2.8 2.8	2.8	5.3 6.0

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	11:15	4.9	Surface	1.0	16.3 16.3	16.3	8.1 8.1	8.1	27.1 26.7	26.9	94.7 94.8	94.8	7.8 7.9	7.9	7.9	4.3 4.2	4.3	4.4	5.9 6.3	6.1	5.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.9	16.3 16.3	16.3	8.1 8.1	8.1	28.9 29.8	29.4	94.8 93.0	93.9	7.8 7.7	7.8		4.4 4.5	4.5		7.8	4.4 4.5		4.5	4.6 4.6	4.6
25-Dec-15	Cloudy	Moderate	12:24	5.3	Surface	1.0	16.7 16.7	16.7	8.0 8.0	8.0	27.4 26.1	26.8	101.4 97.8	99.6	8.2 8.1	8.1	8.1	8.0 7.9	8.0	8.0	7.8 7.2	7.5	7.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.3	16.7 16.7	16.7	8.0 8.0	8.0	30.6 26.9	28.8	99.2 97.1	98.2	8.2 8.1	8.1		8.1	8.0 8.0		8.0	8.1		8.0 8.0	8.0	8.3 8.1
28-Dec-15	Sunny	Moderate	14:27	5.1	Surface	1.0	16.1 16.1	16.1	8.1 8.1	8.1	27.0 27.3	27.1	95.4 95.0	95.2	8.0 8.0	8.0	8.0	5.3 5.5	5.4	5.6	6.3 5.9	6.1	7.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.1	16.1 16.1	16.1	8.1 8.1	8.1	27.3 27.1	27.2	93.2 93.5	93.4	7.8 7.8	7.8		5.8 5.7	5.8		7.8	5.8 5.7		5.8	7.6 8.5	8.1
30-Dec-15	Cloudy	Moderate	15:57	5.1	Surface	1.0	16.0 16.0	16.0	8.2 8.2	8.2	26.2 26.8	26.5	97.0 96.9	97.0	8.2 8.1	8.1	8.1	4.2 4.1	4.2	4.3	2.5 2.5	2.5	3.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.1	16.1 16.0	16.1	8.2 8.2	8.2	27.7 28.0	27.8	96.9 97.0	97.0	8.1 8.1	8.1		4.3 4.3	4.3		8.1	4.3 4.3		4.3	3.8 3.0	3.4

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	12:55	5.0	Surface	1.0	20.3 20.3	20.3	8.1 8.1	8.1	28.7 28.2	28.4	92.4 91.6	92.0	7.1 7.0	7.0	7.0	7.7 7.8	7.8	8.1	4.8 4.5	4.7	4.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	20.3 20.3	20.3	8.0 8.0	8.0	29.5 28.8	29.2	90.5 91.1	90.8	6.9 7.0	6.9		6.9	8.2 8.3		8.3	6.9		8.2 8.3	8.3	6.9	4.4 3.6
4-Dec-15	Cloudy	Moderate	14:47	5.1	Surface	1.0	19.9 19.7	19.8	8.2 8.2	8.2	25.9 24.9	25.4	91.3 92.1	91.7	7.2 7.2	7.2	7.2	4.1 4.0	4.1	4.3	4.2 3.1	3.7	3.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	19.9 20.1	20.0	8.2 8.2	8.2	26.5 28.3	27.4	91.7 91.3	91.5	7.1 7.2	7.1		7.1	4.4 4.4		4.4	7.1		4.4 4.4	4.4	7.1	3.9 3.9
7-Dec-15	Cloudy	Moderate	16:29	4.1	Surface	1.0	19.3 19.4	19.4	8.2 8.2	8.2	32.2 33.4	32.8	95.5 95.8	95.7	7.3 7.3	7.3	7.3	3.6 3.7	3.7	3.8	4.7 5.0	4.9	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	19.3 19.3	19.3	8.2 8.2	8.2	32.7 34.3	33.5	94.8 94.4	94.6	7.2 7.2	7.2		7.2	3.8 3.8		3.8	7.2		3.8 3.8	3.8	7.2	6.4 6.8
9-Dec-15	Rainy	Moderate	16:39	5.0	Surface	1.0	18.6 18.6	18.6	8.2 8.2	8.2	33.3 30.7	32.0	105.6 93.5	99.6	8.0 7.2	7.6	7.6	6.1 6.2	6.2	6.5	3.9 5.0	4.5	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	18.6 18.6	18.6	8.1 8.1	8.1	31.7 35.7	33.7	92.6 96.8	94.7	7.2 7.4	7.3		7.3	6.6 6.7		6.7	7.3		6.6 6.7	6.7	7.3	3.4 4.2
11-Dec-15	Sunny	Moderate	07:37	5.1	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	31.2 31.0	31.1	92.9 93.4	93.2	7.3 7.3	7.3	7.3	9.0 8.6	8.8	9.0	7.3 6.7	7.0	7.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	18.2 18.2	18.2	8.2 8.2	8.2	30.9 31.2	31.1	93.3 93.3	93.3	7.3 7.3	7.3		7.3	9.0 9.1		9.1	7.3		9.0 9.1	9.1	7.3	8.4 7.2
14-Dec-15	Rainy	Moderate	10:02	5.0	Surface	1.0	18.1 18.0	18.0	8.1 8.1	8.1	26.7 26.8	26.8	91.7 92.9	92.3	7.4 7.5	7.4	7.4	6.3 6.4	6.4	6.6	5.5 6.5	6.0	6.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	18.1 18.1	18.1	8.1 8.1	8.1	27.4 29.2	28.3	92.0 92.5	92.3	7.4 7.3	7.4		7.4	6.7 6.6		6.7	7.4		6.7 6.6	6.7	7.4	7.5 6.6
16-Dec-15	Sunny	Moderate	11:18	5.3	Surface	1.0	17.6 17.6	17.6	8.1 8.1	8.1	29.3 29.4	29.4	90.9 93.1	92.0	7.3 7.4	7.4	7.4	8.7 9.0	8.9	9.1	8.3 9.0	8.7	8.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	17.6 17.6	17.6	8.1 8.1	8.1	29.6 29.5	29.6	91.5 91.3	91.4	7.3 7.3	7.3		7.3	9.2 9.1		9.2	7.3		9.2 9.1	9.2	7.3	8.9 9.3
18-Dec-15	Cloudy	Moderate	05:42	5.4	Surface	1.0	15.7 15.7	15.7	8.1 8.1	8.1	27.8 27.8	27.8	95.6 95.6	95.6	8.0 8.0	8.0	8.0	6.8 6.7	6.8	6.9	5.0 6.0	5.5	5.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.4	15.8 15.8	15.8	8.1 8.1	8.1	27.9 27.9	27.9	95.9 95.8	95.9	8.0 8.0	8.0		8.0	7.1 6.7		6.9	8.0		7.1 6.7	6.9	8.0	5.3 6.2
21-Dec-15	Sunny	Moderate	15:07	5.3	Surface	1.0	16.1 16.1	16.1	8.2 8.2	8.2	29.8 30.5	30.2	97.9 98.8	98.4	8.1 8.1	8.1	8.1	3.0 3.0	3.0	3.0	3.9 3.0	3.5	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	16.1 16.1	16.1	8.2 8.2	8.2	30.1 31.5	30.8	98.1 99.3	98.7	8.1 8.1	8.1		8.1	2.9 3.0		3.0	8.1		2.9 3.0	3.0	8.1	3.6 3.0

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-Dec-15	Sunny	Moderate	17:03	5.0	Surface	1.0	16.4 16.4	16.4	8.1 8.1	8.1	24.1 24.1	24.1	95.3 96.0	95.7	8.1 8.1	8.1	8.1	4.4 4.1	4.3	4.6	4.5 3.8	4.2	5.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	16.3 16.3	16.3	8.1 8.1	8.1	26.5 26.0	26.2	96.8 95.3	96.1	8.1 8.0	8.0		4.8 4.8	4.8		8.0	4.8 4.8		4.8	6.4 5.7	6.1	6.1
25-Dec-15	Cloudy	Moderate	07:44	5.1	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	26.1 25.9	26.0	93.6 93.1	93.4	7.8 7.7	7.8	7.8	6.5 6.3	6.4	6.5	6.5 6.4	6.5	7.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.1	16.7 16.7	16.7	8.1 8.1	8.1	26.0 26.0	26.0	93.0 93.1	93.1	7.7 7.7	7.7		6.5 6.5	6.5		7.7	6.5 6.5		6.5	7.4 7.6	7.5	7.5
28-Dec-15	Sunny	Moderate	10:01	5.2	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	28.3 28.1	28.2	94.9 94.9	94.9	7.9 7.9	7.9	7.9	11.8 11.8	11.8	12.1	8.9 9.5	9.2	10.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.2	15.9 15.9	15.9	8.1 8.1	8.1	28.7 28.2	28.5	94.8 94.8	94.8	7.9 7.9	7.9		12.2 12.3	12.3		7.9	11.4 11.8		11.6	11.4 11.8	11.6	
30-Dec-15	Cloudy	Moderate	11:11	5.3	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	28.8 28.6	28.7	94.7 94.9	94.8	7.9 7.9	7.9	7.9	8.7 8.7	8.7	8.7	8.7 10.0	9.4	9.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	16.0 16.0	16.0	8.1 8.1	8.1	28.7 29.1	28.9	94.8 94.3	94.6	7.9 7.8	7.8		8.6 8.8	8.7		7.8	9.1 9.8		9.5	9.1 9.8	9.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	16:32	3.8	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	27.3 27.8	27.5	92.9 91.5	92.2	7.1 7.0	7.1	7.1	4.1 4.2	4.2	4.4	4.3 4.7	4.5	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.8	20.3 20.3	20.3	8.2 8.2	8.2	29.8 29.3	29.5	91.3 92.6	92.0	7.0 7.0	7.0		4.5 4.6	4.6		6.2 5.2	5.7				
4-Dec-15	Cloudy	Moderate	07:08	3.9	Surface	1.0	20.2 20.1	20.2	8.1 8.1	8.1	26.9 28.1	27.5	92.6 93.2	92.9	7.1 7.1	7.1	7.1	3.9 3.8	3.9	4.0	4.0 4.2	4.1	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	20.3 20.5	20.4	8.1 8.1	8.1	29.8 31.1	30.4	90.2 92.5	91.4	7.0 7.0	7.0		4.1 4.1	4.1		4.5 5.5	5.0				
7-Dec-15	Cloudy	Moderate	11:44	4.2	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	31.3 31.9	31.6	93.4 93.2	93.3	7.1 7.1	7.1	7.1	4.7 4.8	4.8	4.9	4.7 4.9	4.8	4.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.2	19.4 19.4	19.4	8.2 8.2	8.2	31.6 34.1	32.8	91.8 91.4	91.6	7.0 7.0	7.0		4.9 5.0	5.0		4.0 5.0	4.5				
9-Dec-15	Rainy	Moderate	12:24	5.3	Surface	1.0	18.1 18.1	18.1	8.2 8.2	8.2	29.8 29.7	29.7	94.3 93.7	94.0	7.4 7.4	7.4	7.4	9.0 9.0	9.0	9.2	6.5 6.0	6.3	6.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	4.3	18.1 18.1	18.1	8.2 8.2	8.2	29.7 30.0	29.9	93.7 93.4	93.6	7.4 7.4	7.4		9.1 9.4	9.3		6.2 5.4	5.8				
11-Dec-15	Sunny	Moderate	11:41	4.1	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	29.6 30.2	29.9	93.4 93.1	93.3	7.4 7.3	7.4	7.4	5.3 5.6	5.5	5.6	3.2 3.4	3.3	3.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.1	18.1 18.1	18.1	8.2 8.2	8.2	31.6 30.8	31.2	94.1 94.2	94.2	7.4 7.4	7.4		5.6 5.5	5.6		3.3 4.5	3.9				
14-Dec-15	Rainy	Moderate	13:41	3.8	Surface	1.0	18.1 18.2	18.2	8.2 8.2	8.2	30.6 29.7	30.2	95.5 95.2	95.4	7.5 7.5	7.5	7.5	5.4 5.3	5.4	5.6	6.9 7.5	7.2	7.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	2.8	18.2 18.2	18.2	8.2 8.1	8.2	30.7 32.0	31.4	95.2 95.7	95.5	7.5 7.5	7.5		5.8 5.7	5.8		7.3 8.3	7.8				
16-Dec-15	Sunny	Moderate	15:30	4.0	Surface	1.0	17.4 17.4	17.4	8.2 8.2	8.2	30.5 30.1	30.3	94.8 93.4	94.1	7.6 7.5	7.5	7.5	6.4 6.5	6.5	6.5	6.8 8.0	7.4	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-					
					Bottom	3.0	17.4 17.5	17.5	8.2 8.2	8.2	30.6 31.3	30.9	95.0 94.3	94.7	7.6 7.5	7.5		6.4 6.5	6.5		7.8 7.7	7.8				
18-Dec-15	Sunny	Moderate	11:43	4.2	Surface	1.0	15.9 15.9	15.9	8.2 8.2	8.2	30.3 30.6	30.4	98.4 98.1	98.3	8.1 8.1	8.1	8.1	7.3 7.3	7.3	7.3	6.8 7.5	7.2	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-					
					Bottom	3.2	15.9 15.9	15.9	8.2 8.2	8.2	30.9 30.4	30.7	98.2 98.2	98.2	8.1 8.1	8.1		7.1 7.2	7.2		8.1 7.6	7.9				
21-Dec-15	Cloudy	Moderate	10:11	4.1	Surface	1.0	15.9 15.9	15.9	8.1 8.2	8.2	28.7 28.8	28.8	95.1 95.2	95.2	7.9 7.9	7.9	7.9	3.5 3.3	3.4	3.5	6.1 4.8	5.5	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-							
					Bottom	3.1	16.0 16.2	16.1	8.1 8.1	8.1	30.2 30.0	30.1	95.3 95.3	95.3	7.8 7.8	7.8		3.5 3.5	3.5		5.6 4.3	5.0				

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	12:16	4.1	Surface	1.0	16.4 16.3	16.4	8.1 8.1	8.1	23.5 23.8	23.6	94.5 94.0	94.3	8.0 8.0	8.0	8.0	3.8 3.8	3.8	4.0	3.3 3.8	3.6	3.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.1	16.3 16.3	16.3	8.1 8.1	8.1	26.6 26.9	26.7	95.3 93.4	94.4	8.0 7.8	7.9		7.9	4.2 4.2		4.2	4.2		4.2	3.5 4.4	4.0
25-Dec-15	Cloudy	Moderate	11:38	5.0	Surface	1.0	16.5 16.5	16.5	8.0 8.0	8.0	23.2 23.9	23.6	94.0 93.1	93.6	7.9 7.9	7.9	7.9	7.5 7.5	7.5	7.6	8.6 9.4	9.0	9.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.0	16.6 16.6	16.6	8.0 8.0	8.0	25.6 25.3	25.5	93.1 92.8	93.0	7.8 7.9	7.8		7.8	7.7 7.5		7.6	7.6		9.6 9.3	9.5	
28-Dec-15	Sunny	Moderate	13:34	4.3	Surface	1.0	15.9 15.9	15.9	8.2 8.2	8.2	30.4 29.4	29.9	95.2 95.4	95.3	7.8 7.9	7.9	7.9	6.7 6.7	6.7	6.8	8.5 9.6	9.1	9.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.3	15.9 15.9	15.9	8.2 8.2	8.2	30.0 31.0	30.5	95.2 95.0	95.1	7.8 7.8	7.8		7.8	6.8 6.8		6.8	6.8		8.6 9.0	8.8	
30-Dec-15	Cloudy	Moderate	15:00	4.3	Surface	1.0	16.0 16.1	16.1	8.2 8.2	8.2	30.1 29.5	29.8	94.2 97.0	95.6	7.7 8.0	7.9	7.9	4.4 4.4	4.4	4.4	4.2 4.4	4.3	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.3	16.0 16.0	16.0	8.2 8.2	8.2	29.9 31.1	30.5	96.1 93.1	94.6	7.9 7.6	7.8		7.8	4.3 4.4		4.4	4.4		4.0 3.9	4.0	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	13:48	4.0	Surface	1.0	20.6 20.5	20.5	8.1 8.1	8.1	24.9 25.5	25.2	96.4 96.4	96.4	7.5 7.5	7.5	7.5	3.7 3.8	3.8	3.9	4.8 3.7	4.3	4.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.0	20.5 20.5	20.5	8.1 8.1	8.1	25.4 25.8	25.6	96.1 96.2	96.2	7.4 7.5	7.4		7.4	3.8 3.9		3.9	7.4		3.8 3.9	3.9	4.6 4.1	4.4
4-Dec-15	Cloudy	Moderate	13:54	3.9	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	29.0 28.6	28.8	96.3 95.9	96.1	7.5 7.4	7.4	7.4	2.9 2.9	2.9	3.0	2.7 3.8	3.3	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.9	19.6 19.5	19.5	8.2 8.2	8.2	30.5 30.0	30.3	96.2 96.2	96.2	7.4 7.4	7.4		7.4	3.1 3.0		3.1	7.4		3.1 3.0	3.1	3.3 3.6	3.5
7-Dec-15	Cloudy	Moderate	15:40	4.3	Surface	1.0	19.4 19.4	19.4	8.3 8.3	8.3	35.1 35.1	35.1	93.4 92.7	93.1	7.0 6.9	6.9	6.9	3.5 3.4	3.5	3.7	5.4 5.9	5.7	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.3	19.4 19.4	19.4	8.3 8.3	8.3	35.2 35.1	35.2	91.9 92.8	92.4	6.9 6.9	6.9		6.9	3.8 3.7		3.8	6.9		3.8 3.7	3.8	6.7 7.8	7.3
9-Dec-15	Rainy	Moderate	15:52	5.1	Surface	1.0	18.0 18.0	18.0	8.1 8.1	8.1	34.3 35.0	34.7	96.0 96.2	96.1	7.4 7.4	7.4	7.4	7.7 7.7	7.7	7.8	4.1 5.1	4.6	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.1	18.0 18.0	18.0	8.1 8.0	8.1	34.7 35.4	35.0	95.9 96.1	96.0	7.4 7.4	7.4		7.4	7.8 7.8		7.8	7.4		7.8 7.8	7.8	5.3 5.7	5.5
11-Dec-15	Sunny	Moderate	08:35	4.3	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	29.3 29.4	29.4	92.7 92.8	92.8	7.3 7.4	7.3	7.3	10.9 10.9	10.9	11.0	9.6 9.4	9.5	9.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.3	18.2 18.2	18.2	8.2 8.2	8.2	29.3 29.4	29.3	92.6 93.2	92.9	7.3 7.4	7.4		7.4	10.8 11.2		11.0	7.4		10.8 11.2	11.0	9.7 8.6	9.2
14-Dec-15	Rainy	Moderate	10:55	4.0	Surface	1.0	18.2 18.1	18.2	8.1 8.1	8.1	26.8 27.0	26.9	97.7 98.2	98.0	7.8 7.9	7.9	7.9	8.5 8.6	8.6	8.8	8.4 8.0	8.2	8.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.0	18.2 18.2	18.2	8.1 8.1	8.1	27.1 29.1	28.1	96.1 96.3	96.2	7.7 7.7	7.7		7.7	8.8 8.9		8.9	7.7		8.8 8.9	8.9	8.4 8.6	8.5
16-Dec-15	Sunny	Moderate	12:12	4.4	Surface	1.0	17.5 17.5	17.5	8.1 8.1	8.1	27.0 26.9	26.9	92.0 91.9	92.0	7.5 7.5	7.5	7.5	16.4 16.9	16.7	17.0	14.9 13.6	14.3	14.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.4	17.5 17.5	17.5	8.1 8.1	8.1	26.8 26.9	26.9	91.9 93.1	92.5	7.5 7.6	7.5		7.5	16.9 17.4		17.2	7.5		16.9 17.4	17.2	14.8 14.3	14.6
18-Dec-15	Cloudy	Moderate	06:36	4.1	Surface	1.0	16.6 16.6	16.6	8.1 8.1	8.1	27.8 27.9	27.9	94.6 95.4	95.0	7.8 7.9	7.8	7.8	5.0 4.8	4.9	5.0	4.5 5.2	4.9	4.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.1	16.6 16.6	16.6	8.1 8.1	8.1	27.8 27.9	27.9	94.0 93.8	93.9	7.8 7.7	7.7		7.7	5.2 5.0		5.1	7.7		5.2 5.0	5.1	5.0 4.4	4.7
21-Dec-15	Sunny	Moderate	14:12	4.3	Surface	1.0	16.2 16.3	16.3	8.3 8.3	8.3	34.4 33.8	34.1	94.5 97.1	95.8	7.5 7.8	7.7	7.7	3.2 3.2	3.2	3.2	4.0 5.1	4.6	3.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.3	16.0 16.2	16.1	8.3 8.3	8.3	34.8 34.1	34.5	95.8 96.1	96.0	7.7 7.7	7.7		7.7	3.3 3.0		3.2	7.7		3.3 3.0	3.2	3.8 2.6	3.2

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	16:13	4.2	Surface	1.0	16.6 16.5	16.5	8.2 8.2	8.2	27.9 27.5	27.7	96.3 95.5	95.9	7.9 7.9	7.9	7.9	6.6 6.7	6.7	6.9	3.9 4.9	4.4	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	16.3 16.4	16.3	8.1 8.1	8.1	31.8 30.3	31.1	95.9 95.6	95.8	7.8 7.8	7.8		7.0 7.2	7.1		7.8	7.0 7.2		7.1	7.8	4.7 3.5
25-Dec-15	Cloudy	Moderate	08:23	4.3	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	26.1 25.4	25.8	95.5 95.5	95.5	8.0 8.0	8.0	8.0	8.0 7.9	8.0	8.0	9.1 9.8	9.5	9.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.3	16.7 16.8	16.7	8.1 8.1	8.1	25.6 25.5	25.5	95.4 95.4	95.4	8.0 7.9	7.9		7.9 8.0	8.0		7.9	7.9 8.0		8.0	7.9	9.0 9.2
28-Dec-15	Sunny	Moderate	10:50	4.3	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	27.7 27.9	27.8	94.8 95.1	95.0	7.9 7.9	7.9	7.9	7.7 7.6	7.7	7.9	18.9 18.7	18.8	19.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.3	16.0 16.0	16.0	8.1 8.1	8.1	27.8 28.2	28.0	94.5 95.1	94.8	7.9 7.9	7.9		8.0 8.1	8.1		7.9	8.0 8.1		8.1	7.9	19.1 19.5
30-Dec-15	Cloudy	Moderate	12:05	4.4	Surface	1.0	16.0 16.0	16.0	8.1 8.1	8.1	27.4 27.5	27.5	95.6 95.7	95.7	8.0 8.0	8.0	8.0	6.3 6.5	6.4	6.5	7.2 7.3	7.3	6.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.4	16.0 16.0	16.0	8.1 8.1	8.1	27.4 27.3	27.4	95.6 95.5	95.6	8.0 8.0	8.0		6.6 6.6	6.6		8.0	6.6 6.6		6.6	8.0	5.9 4.8

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-Dec-15	Sunny	Moderate	17:40	3.8	Surface	1.0	20.5 20.4	20.4	8.1 8.1	8.1	21.3 21.2	21.3	92.9 93.1	93.0	7.4 7.4	7.4	7.4	4.1 4.2	4.2	4.3	2.9 2.4	2.7	3.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.8	20.4 20.4	20.4	8.1 8.1	8.1	23.0 22.9	22.9	93.0 93.3	93.2	7.3 7.4	7.3		4.3 4.3	4.3		3.4 3.0	3.2				
4-Dec-15	Cloudy	Moderate	05:38	3.8	Surface	1.0	20.0 19.9	20.0	8.1 8.1	8.1	29.4 29.5	29.5	90.0 93.0	91.5	6.9 6.9	6.9	6.9	4.4 4.3	4.4	4.6	3.1 3.5	3.3	3.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	20.5 20.3	20.4	8.1 8.1	8.1	33.5 33.6	33.6	91.6 89.4	90.5	6.8 6.8	6.8		4.8 4.7	4.8		2.4 4.2	3.3				
7-Dec-15	Cloudy	Moderate	09:41	3.9	Surface	1.0	19.4 19.4	19.4	8.1 8.2	8.2	35.3 35.3	35.3	95.6 95.0	95.3	7.1 7.1	7.1	7.1	2.8 2.8	2.8	2.8	3.9 4.6	4.3	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	19.4 19.4	19.4	8.1 8.2	8.2	35.3 35.4	35.4	94.6 94.8	94.7	7.0 7.0	7.0		2.8 2.8	2.8		4.9 3.7	4.3				
9-Dec-15	Rainy	Moderate	10:51	5.3	Surface	1.0	18.8 18.8	18.8	8.2 8.2	8.2	35.8 35.8	35.8	94.0 96.5	95.3	7.1 7.3	7.2	7.2	4.0 4.0	4.0	4.1	4.3 3.3	3.8	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	4.3	18.8 18.8	18.8	8.2 8.2	8.2	35.8 35.9	35.8	93.4 94.0	93.7	7.0 7.1	7.1		4.2 4.2	4.2		5.3 4.1	4.7				
11-Dec-15	Sunny	Moderate	13:07	4.4	Surface	1.0	18.2 18.2	18.2	8.2 8.2	8.2	28.7 28.4	28.5	92.5 92.4	92.5	7.3 7.4	7.3	7.3	5.2 5.4	5.3	5.4	5.3 3.8	4.6	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.4	18.3 18.2	18.3	8.2 8.2	8.2	29.0 28.9	28.9	92.2 92.4	92.3	7.3 7.3	7.3		5.4 5.6	5.5		4.6 3.3	4.0				
14-Dec-15	Rainy	Moderate	14:59	4.2	Surface	1.0	17.9 17.9	17.9	8.1 8.1	8.1	20.1 20.4	20.2	92.1 93.0	92.6	7.8 7.7	7.7	7.7	5.4 5.5	5.5	5.5	5.3 5.8	5.6	5.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.2	18.0 18.1	18.1	8.1 8.1	8.1	25.0 24.6	24.8	91.9 91.9	91.9	7.6 7.5	7.5		5.5 5.5	5.5		5.8 6.2	6.0				
16-Dec-15	Sunny	Moderate	16:51	4.3	Surface	1.0	17.6 17.6	17.6	8.2 8.2	8.2	28.5 28.5	28.5	92.2 91.9	92.1	7.4 7.4	7.4	7.4	3.5 3.6	3.6	3.6	11.0 11.8	11.4	11.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.3	17.6 17.7	17.6	8.2 8.2	8.2	28.6 29.0	28.8	92.6 92.6	92.6	7.4 7.4	7.4		3.5 3.4	3.5		11.7 11.0	11.4				
18-Dec-15	Sunny	Moderate	13:08	4.1	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	28.7 28.7	28.7	93.2 95.9	94.6	7.6 7.9	7.7	7.7	5.7 5.6	5.7	6.0	4.2 4.9	4.6	4.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.1	16.6 16.6	16.6	8.1 8.1	8.1	28.9 28.7	28.8	95.0 95.6	95.3	7.8 7.8	7.8		6.3 6.0	6.2		5.0 5.2	5.1				
21-Dec-15	Cloudy	Moderate	08:47	4.2	Surface	1.0	16.4 16.4	16.4	8.1 8.1	8.1	35.7 35.7	35.7	96.0 97.4	96.7	7.6 7.7	7.6	7.6	3.9 3.9	3.9	3.9	4.8 5.0	4.9	4.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-				
					Bottom	3.2	16.4 16.4	16.4	8.1 8.2	8.2	35.7 35.8	35.8	96.4 98.9	97.7	7.6 7.8	7.7		3.9 3.9	3.9		4.3 5.0	4.7				

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	10:32	4.2	Surface	1.0	16.3 16.3	16.3	8.1 8.1	8.1	31.8 31.9	31.9	97.0 96.5	96.8	7.7 7.8	7.8	7.8	3.1 3.1	3.1	3.2	4.0 4.2	4.1	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	16.3 16.3	16.3	8.1 8.1	8.1	34.5 34.1	34.3	94.8 95.3	95.1	7.7 7.7	7.7		7.7	3.2 3.2		3.2	5.8 4.2		5.0		
25-Dec-15	Cloudy	Moderate	12:52	5.1	Surface	1.0	16.7 16.7	16.7	8.1 8.1	8.1	24.1 24.1	24.1	95.5 95.3	95.4	8.0 8.0	8.0	8.0	6.3 6.4	6.4	6.5	8.0 8.1	8.1	7.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.1	16.7 16.7	16.7	8.1 8.1	8.1	24.2 24.2	24.2	95.4 95.2	95.3	8.0 8.0	8.0		8.0	6.4 6.5		6.5	7.4 7.7		7.6		
28-Dec-15	Sunny	Moderate	14:54	4.2	Surface	1.0	16.0 16.0	16.0	8.2 8.1	8.2	25.4 25.3	25.3	94.7 94.6	94.7	8.0 8.0	8.0	8.0	5.4 5.2	5.3	5.4	6.0 6.0	6.0	6.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.2	16.0 16.0	16.0	8.1 8.2	8.1	25.3 25.3	25.3	94.5 94.5	94.5	8.0 8.0	8.0		8.0	5.6 5.4		5.5	7.6 7.6		7.6		
30-Dec-15	Cloudy	Moderate	16:27	4.3	Surface	1.0	16.1 16.1	16.1	8.2 8.2	8.2	26.4 26.4	26.4	96.4 96.2	96.3	8.1 8.1	8.1	8.1	4.6 4.6	4.6	4.8	4.4 4.9	4.7	4.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.3	16.0 16.0	16.0	8.2 8.2	8.2	26.5 26.5	26.5	96.0 96.3	96.2	8.1 8.1	8.1		8.1	5.0 4.7		4.9	4.9 4.3		4.6		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	12:24	3.9	Surface	1.0	20.3 20.4	20.4	8.1 8.1	8.1	29.1 28.8	28.9	92.6 92.5	92.6	7.1 7.1	7.1	7.1	5.2 5.1	5.2	5.3	10.4 9.1	9.8	9.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	20.3 20.3	20.3	8.0 8.1	8.1	29.8 29.7	29.8	92.1 92.0	92.1	7.0 7.0	7.0		7.0	5.4 5.3		5.4	7.0		5.4 5.3	5.4	9.1 9.9	9.5
4-Dec-15	Cloudy	Moderate	15:20	3.8	Surface	1.0	20.0 19.7	19.8	8.2 8.2	8.2	23.5 22.6	23.0	91.8 90.3	91.1	7.2 7.1	7.2	7.2	5.7 5.7	5.7	6.0	4.5 4.1	4.3	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	20.2 20.0	20.1	8.1 8.1	8.1	26.4 25.6	26.0	90.8 90.7	90.8	7.0 7.2	7.1		7.1	6.1 6.2		6.2	7.1		6.1 6.2	6.2	6.0 6.6	6.3
7-Dec-15	Cloudy	Moderate	17:00	4.1	Surface	1.0	19.4 19.4	19.4	8.2 8.2	8.2	29.9 29.9	29.9	94.0 94.1	94.1	7.3 7.3	7.3	7.3	3.7 3.8	3.8	3.9	5.1 4.7	4.9	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	19.4 19.4	19.4	8.2 8.2	8.2	30.1 29.9	30.0	94.2 94.1	94.2	7.3 7.3	7.3		7.3	3.9 3.9		3.9	7.3		3.9 3.9	3.9	6.8 6.8	6.8
9-Dec-15	Rainy	Moderate	17:06	5.1	Surface	1.0	18.7 18.7	18.7	8.2 8.2	8.2	29.6 29.7	29.6	93.5 93.4	93.5	7.3 7.3	7.3	7.3	5.2 5.0	5.1	5.2	7.6 7.3	7.5	7.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	18.8 18.8	18.8	8.2 8.2	8.2	29.7 29.7	29.7	92.8 91.5	92.2	7.3 7.2	7.2		7.2	5.2 5.2		5.2	7.2		5.2 5.2	5.2	6.9 6.4	6.7
11-Dec-15	Sunny	Moderate	07:08	4.3	Surface	1.0	18.2 18.3	18.3	8.1 8.1	8.1	35.6 35.5	35.6	96.7 95.1	95.9	7.4 7.2	7.3	7.3	11.6 11.4	11.5	11.6	11.1 11.2	11.2	11.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.3	18.3 18.2	18.3	8.1 8.1	8.1	35.6 35.6	35.6	96.1 99.0	97.6	7.3 7.5	7.4		7.4	11.7 11.5		11.6	7.4		11.7 11.5	11.6	11.1 11.0	11.1
14-Dec-15	Rainy	Moderate	09:30	4.3	Surface	1.0	18.2 18.2	18.2	8.1 8.1	8.1	33.2 32.9	33.0	94.3 94.6	94.5	7.3 7.3	7.3	7.3	7.8 7.7	7.8	8.0	8.5 8.7	8.6	8.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.3	18.2 18.2	18.2	8.0 8.1	8.1	33.9 33.8	33.8	94.7 94.4	94.6	7.3 7.3	7.3		7.3	8.2 8.1		8.2	7.3		8.2 8.1	8.2	8.9 8.8	8.9
16-Dec-15	Sunny	Moderate	10:49	4.4	Surface	1.0	17.6 17.6	17.6	8.0 8.0	8.0	33.0 32.9	33.0	103.0 98.1	100.6	8.1 7.7	7.9	7.9	18.8 18.6	18.7	18.6	21.7 21.9	21.8	22.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.4	17.5 17.6	17.6	8.0 8.0	8.0	33.0 33.0	33.0	110.4 101.1	105.8	8.7 7.9	8.3		8.3	18.4 18.6		18.5	8.3		18.4 18.6	18.5	23.5 22.2	22.9
18-Dec-15	Cloudy	Moderate	05:13	4.1	Surface	1.0	15.7 15.6	15.7	8.1 8.1	8.1	28.7 28.9	28.8	102.3 107.5	104.9	8.5 9.0	8.8	8.8	7.0 6.9	7.0	7.0	6.8 6.7	6.8	6.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	15.7 15.7	15.7	8.1 8.1	8.1	28.9 29.1	29.0	104.1 110.9	107.5	8.7 9.2	9.0		9.0	7.0 6.9		7.0	9.0		7.0 6.9	7.0	6.3 7.0	6.7
21-Dec-15	Sunny	Moderate	15:32	4.3	Surface	1.0	16.4 16.4	16.4	8.2 8.2	8.2	28.5 28.5	28.5	95.1 94.9	95.0	7.8 7.8	7.8	7.8	4.6 4.6	4.6	4.7	5.8 4.1	5.0	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.3	16.4 16.4	16.4	8.2 8.2	8.2	28.5 28.5	28.5	95.2 95.5	95.4	7.8 7.9	7.9		7.9	4.7 4.6		4.7	7.9		4.7 4.6	4.7	5.8 5.4	5.6

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	17:39	4.4	Surface	1.0	16.5 16.5	16.5	8.1 8.1	8.1	26.0 26.0	26.0	95.7 95.8	95.8	8.0 8.0	8.0	8.0	5.8 5.7	5.8	6.1	5.2 5.6	5.4	6.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.4	16.5 16.5	16.5	8.1 8.1	8.1	26.1 26.2	26.2	95.6 95.8	95.7	8.0 8.0	8.0		8.0	6.3 6.4		6.4	8.0		6.3 6.4	6.4	8.0
25-Dec-15	Cloudy	Moderate	07:23	5.0	Surface	1.0	16.7 16.7	16.7	8.0 8.0	8.0	31.2 31.2	31.2	98.3 102.9	100.6	7.9 8.2	8.1	8.1	8.2 8.4	8.3	8.3	7.9 7.7	7.8	7.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	16.8 16.8	16.8	8.0 8.0	8.0	31.8 31.9	31.9	97.3 99.3	98.3	7.8 8.0	7.9		7.9	8.2 8.4		8.3	7.9		8.2 8.4	8.3	7.9
28-Dec-15	Sunny	Moderate	09:28	4.4	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	31.9 30.9	31.4	95.9 95.7	95.8	7.8 7.8	7.8	7.8	18.7 18.9	18.8	19.0	21.5 22.1	21.8	22.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.4	15.9 15.9	15.9	8.1 8.1	8.1	32.2 31.8	32.0	96.0 95.4	95.7	7.8 7.8	7.8		7.8	19.2 19.1		19.2	7.8		19.2 19.1	19.2	7.8
30-Dec-15	Cloudy	Moderate	10:40	4.4	Surface	1.0	15.9 15.9	15.9	8.1 8.1	8.1	32.6 32.7	32.7	100.7 98.7	99.7	8.2 8.0	8.1	8.1	6.8 6.8	6.8	6.9	7.0 6.2	6.6	6.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.4	15.9 15.9	15.9	8.1 8.1	8.1	32.7 32.7	32.7	102.8 99.5	101.2	8.3 8.1	8.2		8.2	7.0 7.0		7.0	8.2		7.0 7.0	7.0	8.2

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	18:31	6.6	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	27.1 27.1	27.1	86.3 87.1	86.7	6.2 6.3	6.3	6.2	2.7 2.6	2.7	2.7	3.3 3.6	3.5	3.1
					Middle	3.3	23.9 23.9	23.9	8.1 8.1	8.1	28.1 28.0	28.1	84.1 86.5	85.3	6.0 6.2	6.1		2.7 2.7	2.7		2.6 3.0	2.8	
					Bottom	5.6	23.9 23.9	23.9	8.1 8.1	8.1	28.7 28.8	28.8	87.1 84.7	85.9	6.2 6.1	6.1		2.8 2.8	2.8		3.1 2.8	3.0	
4-Dec-15	Cloudy	Moderate	05:32	6.8	Surface	1.0	23.1 23.3	23.2	8.1 8.1	8.1	26.5 26.4	26.5	84.2 85.9	85.1	6.2 6.2	6.2	6.2	2.1 2.0	2.1	2.2	2.5 2.8	2.7	2.6
					Middle	3.4	23.6 23.7	23.6	8.1 8.1	8.1	29.0 29.2	29.1	84.7 85.7	85.2	6.1 6.2	6.1		2.2 2.1	2.2		2.9 2.8	2.9	
					Bottom	5.8	23.8 23.3	23.6	8.1 8.1	8.1	29.3 29.7	29.5	85.1 84.9	85.0	6.1 6.1	6.1		2.2 2.1	2.2		2.2 2.0	2.1	
7-Dec-15	Cloudy	Moderate	09:25	6.5	Surface	1.0	22.9 22.9	22.9	8.2 8.2	8.2	30.2 30.2	30.2	88.7 90.8	89.8	6.4 6.6	6.5	6.5	3.2 3.1	3.2	3.2	3.5 3.6	3.6	4.3
					Middle	3.3	22.9 22.9	22.9	8.2 8.2	8.2	30.2 30.2	30.2	90.6 88.2	89.4	6.5 6.4	6.5		3.2 3.2	3.2		5.3 4.4	4.9	
					Bottom	5.5	22.9 22.9	22.9	8.2 8.2	8.2	30.2 30.2	30.2	86.4 87.0	86.7	6.2 6.3	6.3		3.2 3.1	3.2		5.1 3.9	4.5	
9-Dec-15	Rainy	Moderate	10:56	6.6	Surface	1.0	22.3 22.3	22.3	8.1 8.2	8.2	31.1 31.0	31.1	85.7 86.3	86.0	6.2 6.3	6.2	6.2	3.1 3.1	3.1	3.2	3.8 3.7	3.8	4.0
					Middle	3.3	22.4 22.4	22.4	8.1 8.2	8.1	31.1 31.1	31.1	84.7 85.3	85.0	6.1 6.2	6.2		3.3 3.2	3.3		4.1 4.4	4.3	
					Bottom	5.6	22.4 22.4	22.4	8.1 8.1	8.1	31.2 31.2	31.2	84.5 85.3	84.9	6.1 6.2	6.2		3.3 3.2	3.3		3.2 4.8	4.0	
11-Dec-15	Sunny	Moderate	13:44	6.5	Surface	1.0	22.1 22.0	22.1	8.2 8.2	8.2	31.1 31.2	31.2	86.0 84.9	85.5	6.3 6.2	6.2	6.2	4.5 4.7	4.6	4.5	5.2 4.7	5.0	5.3
					Middle	3.3	21.9 21.9	21.9	8.2 8.2	8.2	31.3 31.3	31.3	84.6 84.0	84.3	6.2 6.1	6.2		4.7 4.6	4.7		5.1 5.5	5.3	
					Bottom	5.5	22.1 22.1	22.1	8.2 8.2	8.2	31.4 31.5	31.5	84.3 84.9	84.6	6.1 6.2	6.2		4.5 4.1	4.3		4.9 6.1	5.5	
14-Dec-15	Rainy	Moderate	15:51	6.6	Surface	1.0	21.6 21.6	21.6	8.2 8.2	8.2	28.9 28.8	28.8	89.5 91.0	90.3	6.7 6.8	6.7	6.7	3.9 3.9	3.9	4.2	4.1 3.1	3.6	4.5
					Middle	3.3	21.7 21.7	21.7	8.2 8.2	8.2	29.0 29.0	29.0	87.9 89.1	88.5	6.5 6.6	6.6		4.5 4.3	4.4		4.5 4.4	4.5	
					Bottom	5.6	21.8 21.7	21.8	8.2 8.2	8.2	30.3 30.4	30.3	87.5 88.4	88.0	6.4 6.5	6.5		4.4 4.2	4.3		4.8 6.0	5.4	
16-Dec-15	Sunny	Moderate	17:28	6.6	Surface	1.0	20.9 21.0	21.0	8.2 8.2	8.2	28.0 28.0	28.0	88.1 86.7	87.4	6.7 6.6	6.6	6.7	4.8 4.6	4.7	4.6	6.5 6.4	6.5	7.1
					Middle	3.3	21.1 21.0	21.0	8.2 8.2	8.2	28.1 28.1	28.1	85.5 91.4	88.5	6.5 6.9	6.7		4.7 4.7	4.6		6.0 7.3	6.7	
					Bottom	5.6	21.4 21.0	21.2	8.2 8.2	8.2	29.5 28.1	28.8	85.0 86.5	85.8	6.3 6.6	6.4		4.3 4.5	4.4		7.9 8.5	8.2	
18-Dec-15	Sunny	Moderate	13:45	6.5	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.6 30.6	30.6	87.6 87.1	87.4	6.6 6.6	6.6	6.6	4.2 4.2	4.2	4.3	5.1 6.1	5.6	5.6
					Middle	3.3	20.3 20.3	20.3	8.2 8.2	8.2	30.7 30.8	30.8	86.9 86.8	86.9	6.6 6.6	6.6		4.4 4.2	4.3		4.9 5.8	5.4	
					Bottom	5.5	20.4 20.3	20.4	8.2 8.2	8.2	30.9 30.8	30.8	87.1 87.5	87.3	6.6 6.6	6.6		4.2 4.3	4.3		5.7 5.8	5.8	
21-Dec-15	Cloudy	Moderate	16:29	6.7	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	30.4 30.5	30.5	86.7 86.1	86.4	6.6 6.5	6.5	6.5	2.1 2.1	2.1	2.4	9.0 8.2	8.6	6.2
					Middle	3.4	20.2 20.2	20.2	8.2 8.2	8.2	30.6 30.6	30.6	86.0 86.2	86.1	6.5 6.5	6.5		2.4 2.4	2.4		5.4 3.8	4.6	
					Bottom	5.7	20.2 20.2	20.2	8.2 8.2	8.2	30.7 30.7	30.7	86.4 85.7	86.1	6.5 6.5	6.5		2.5 2.7	2.6		5.2 5.6	5.4	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-Dec-15	Sunny	Moderate	10:15	6.4	Surface	1.0	20.1 20.2	20.2	8.1 8.1	8.1	29.4 29.4	29.4	87.9 90.8	89.4	6.7 6.9	6.8	6.8	3.3 3.0	3.2	3.3	4.2 3.0	3.6	3.7
					Middle	3.2	20.1 20.1	20.1	8.1 8.1	8.1	29.6 29.6	29.6	86.3 88.1	87.2	6.6 6.7	6.7		3.3 3.3	3.3		4.4 3.1	3.8	
					Bottom	5.4	20.1 20.1	20.1	8.1 8.1	8.1	29.6 29.9	29.7	87.7 86.3	87.0	6.7 6.6	6.6		3.4 3.2	3.3		3.7 3.4	3.6	
25-Dec-15	Cloudy	Moderate	13:41	6.3	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	27.4 27.4	27.4	86.6 86.2	86.4	6.7 6.6	6.7	6.7	5.0 5.0	5.0	5.1	5.2 5.6	5.4	5.6
					Middle	3.2	20.3 20.3	20.3	8.2 8.2	8.2	29.0 29.0	29.0	86.7 86.1	86.4	6.6 6.6	6.6		5.1 5.0	5.1		5.7 5.2	5.5	
					Bottom	5.3	20.2 20.3	20.3	8.2 8.1	8.2	29.3 29.2	29.2	86.9 87.4	87.2	6.6 6.7	6.6		5.1 5.2	5.2		6.3 5.7	6.0	
28-Dec-15	Sunny	Moderate	15:31	6.4	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	28.6 28.6	28.6	86.3 85.7	86.0	6.7 6.6	6.6	6.6	4.2 4.2	4.2	4.2	3.9 3.8	3.9	5.2
					Middle	3.2	19.8 19.8	19.8	8.2 8.2	8.2	29.1 29.1	29.1	86.1 85.0	85.6	6.6 6.5	6.6		4.1 4.3	4.2		4.7 5.8	5.3	
					Bottom	5.4	19.7 19.7	19.7	8.2 8.2	8.2	29.0 29.2	29.1	86.8 85.9	86.4	6.7 6.6	6.6		4.2 4.3	4.3		5.7 7.1	6.4	
30-Dec-15	Cloudy	Moderate	16:51	6.6	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.1 29.1	29.1	89.0 90.9	90.0	6.9 7.0	6.9	7.0	3.7 3.5	3.6	4.0	5.6 4.1	4.9	3.9
					Middle	3.3	19.7 19.7	19.7	8.2 8.2	8.2	29.4 29.5	29.4	90.5 91.3	90.9	7.0 7.0	7.0		4.1 3.9	4.0		3.2 4.7	4.0	
					Bottom	5.6	19.7 19.7	19.7	8.2 8.2	8.2	29.5 29.6	29.5	88.7 87.7	88.2	6.8 6.7	6.8		4.4 4.5	4.5		2.1 3.5	2.8	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-Dec-15	Sunny	Moderate	11:29	6.6	Surface	1.0	23.7 23.7	23.7	8.1 8.1	8.1	25.8 25.8	25.8	83.9 84.3	84.1	6.1 6.2	6.1	6.1	3.9 3.8	3.9	3.9	3.3 3.3	3.3	3.7
					Middle	3.3	23.8 23.8	23.8	8.0 8.1	8.1	26.8 26.8	26.8	84.0 84.2	84.1	6.1 6.1	6.1		3.8 4.0	3.9		4.0 4.3	4.2	
					Bottom	5.6	23.8 23.8	23.8	8.0 8.0	8.0	26.9 26.9	26.9	84.0 84.0	84.0	6.1 6.1	6.1		3.8 3.9	3.9		4.2 2.9	3.6	
4-Dec-15	Cloudy	Moderate	15:11	6.4	Surface	1.0	23.4 23.4	23.4	8.2 8.2	8.2	28.8 29.1	28.9	84.2 85.3	84.8	6.1 6.1	6.1	6.1	2.2 2.1	2.2	2.3	2.1 3.0	2.6	2.8
					Middle	3.2	23.7 23.6	23.7	8.1 8.1	8.1	29.9 29.7	29.8	83.4 84.2	83.8	6.0 6.0	6.0		2.5 2.3	2.4		3.0 2.7	2.9	
					Bottom	5.4	23.9 23.6	23.8	8.1 8.1	8.1	30.7 30.9	30.8	84.0 85.2	84.6	5.9 6.1	6.0		2.3 2.4	2.4		2.8 3.0	2.9	
7-Dec-15	Cloudy	Moderate	17:11	6.4	Surface	1.0	22.6 22.6	22.6	8.2 8.2	8.2	31.0 30.9	31.0	89.5 91.3	90.4	6.4 6.6	6.5	6.5	2.4 2.4	2.4	2.5	3.8 4.3	4.1	4.5
					Middle	3.2	22.7 22.8	22.7	8.2 8.2	8.2	31.4 31.4	31.4	90.2 89.1	89.7	6.5 6.4	6.5		2.5 2.6	2.6		4.8 3.7	4.3	
					Bottom	5.4	22.6 22.8	22.7	8.2 8.2	8.2	31.4 31.7	31.6	88.2 87.9	88.1	6.4 6.4	6.4		2.6 2.6	2.6		4.3 5.6	5.0	
9-Dec-15	Rainy	Moderate	18:00	6.5	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	31.2 31.2	31.2	88.3 85.0	86.7	6.4 6.2	6.3	6.3	6.6 6.7	6.7	6.7	6.7 6.5	6.6	6.7
					Middle	3.3	22.3 22.3	22.3	8.2 8.2	8.2	31.2 31.2	31.2	85.1 85.3	85.2	6.2 6.2	6.2		6.7 6.7	6.7		7.2 7.0	7.1	
					Bottom	5.5	22.3 22.3	22.3	8.2 8.2	8.2	31.2 31.2	31.2	84.7 85.6	85.2	6.1 6.2	6.2		6.7 6.7	6.7		6.9 6.1	6.5	
11-Dec-15	Sunny	Moderate	06:28	6.4	Surface	1.0	22.0 22.0	22.0	8.1 8.1	8.1	30.0 30.0	30.0	84.2 84.6	84.4	6.2 6.2	6.2	6.2	5.4 5.1	5.3	5.6	10.0 9.3	9.7	9.6
					Middle	3.2	22.0 22.0	22.0	8.1 8.1	8.1	30.0 30.0	30.0	84.2 84.3	84.3	6.2 6.2	6.2		5.8 5.5	5.7		9.6 10.0	9.8	
					Bottom	5.4	22.0 22.0	22.0	8.1 8.1	8.1	30.0 30.0	30.0	84.1 84.5	84.3	6.2 6.2	6.2		5.9 5.4	5.7		9.5 9.3	9.4	
14-Dec-15	Rainy	Moderate	08:41	6.7	Surface	1.0	21.7 21.7	21.7	8.1 8.1	8.1	28.5 28.5	28.5	86.6 86.0	86.3	6.5 6.4	6.4	6.4	6.9 6.7	6.8	6.7	10.6 10.1	10.4	10.1
					Middle	3.4	21.7 21.7	21.7	8.1 8.1	8.1	28.6 28.7	28.7	85.8 86.1	86.0	6.4 6.4	6.4		6.7 6.9	6.8		10.9 10.1	10.5	
					Bottom	5.7	21.7 21.7	21.7	8.1 8.1	8.1	28.7 28.6	28.6	86.1 85.7	85.9	6.4 6.4	6.4		6.6 6.5	6.6		9.6 9.2	9.4	
16-Dec-15	Sunny	Moderate	10:17	6.7	Surface	1.0	21.2 21.2	21.2	8.1 8.1	8.1	28.0 28.1	28.1	85.4 88.0	86.7	6.4 6.6	6.5	6.5	4.5 4.2	4.4	4.4	6.1 7.0	6.6	7.4
					Middle	3.4	21.2 21.2	21.2	8.1 8.1	8.1	28.1 28.0	28.0	85.9 87.0	86.5	6.5 6.6	6.5		4.2 4.3	4.3		7.9 7.6	7.8	
					Bottom	5.7	21.2 21.2	21.2	8.1 8.0	8.1	28.0 28.1	28.1	84.9 87.9	86.4	6.4 6.6	6.5		4.3 4.4	4.4		7.0 8.8	7.9	
18-Dec-15	Cloudy	Moderate	04:26	6.4	Surface	1.0	19.9 19.9	19.9	8.2 8.2	8.2	29.3 29.3	29.3	92.3 91.5	91.9	7.0 7.0	7.0	6.9	7.2 7.1	7.2	7.2	2.3 2.8	2.6	2.4
					Middle	3.2	20.1 20.1	20.1	8.1 8.2	8.2	29.6 29.6	29.6	89.5 89.4	89.5	6.8 6.9	6.8		7.1 7.2	7.2		2.1 2.4	2.3	
					Bottom	5.4	20.2 20.0	20.1	8.1 8.2	8.2	29.8 29.7	29.7	87.4 87.7	87.6	6.6 6.7	6.7		7.1 7.4	7.3		2.1 2.4	2.3	
21-Dec-15	Sunny	Moderate	07:56	6.6	Surface	1.0	20.2 20.2	20.2	8.1 8.1	8.1	29.8 29.9	29.9	84.7 85.0	84.9	6.4 6.5	6.4	6.4	2.4 2.4	2.4	2.5	4.9 5.5	5.2	4.5
					Middle	3.3	20.2 20.2	20.2	8.1 8.1	8.1	29.9 29.8	29.9	84.6 84.1	84.4	6.4 6.4	6.4		2.4 2.4	2.4		4.0 4.8	4.4	
					Bottom	5.6	20.2 20.2	20.2	8.1 8.1	8.1	29.8 29.9	29.8	83.8 84.3	84.1	6.4 6.4	6.4		2.8 2.6	2.7		3.2 4.3	3.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-Dec-15	Sunny	Moderate	17:35	6.6	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	28.4 28.4	28.4	91.6 90.1	90.9	7.0 6.9	7.0	6.9	3.4 3.6	3.5	3.9	2.6 3.7	3.2	4.2	
					Middle	3.3	20.1 20.1	20.1	8.2 8.2	8.2	29.9 29.8	29.9	89.4 90.0	89.7	6.8 6.9	6.8		4.1 4.0	4.1		4.1 4.0	3.3 4.0		3.7
					Bottom	5.6	20.1 20.1	20.1	8.2 8.2	8.2	30.8 30.9	30.9	89.2 91.4	90.3	6.8 6.9	6.8		4.1 4.1	4.1		4.1 6.4	4.9 6.4		5.7
25-Dec-15	Cloudy	Moderate	06:51	6.5	Surface	1.0	20.2 20.1	20.2	8.1 8.1	8.1	26.6 26.5	26.6	87.0 87.6	87.3	6.7 6.8	6.8	6.7	8.5 8.7	8.6	8.7	5.2 6.6	5.9	7.3	
					Middle	3.3	20.3 20.3	20.3	8.1 8.1	8.1	28.1 28.1	28.1	86.9 86.4	86.7	6.7 6.6	6.6		8.8 8.5	8.7		7.8 8.0	7.9		
					Bottom	5.5	20.3 20.2	20.3	8.1 8.1	8.1	28.3 28.4	28.3	86.1 87.1	86.6	6.6 6.7	6.6		8.6 8.8	8.7		7.7 8.3	8.0		
28-Dec-15	Sunny	Moderate	08:31	6.4	Surface	1.0	19.5 19.5	19.5	8.1 8.1	8.1	27.6 27.7	27.7	88.2 88.0	88.1	6.9 6.9	6.9	6.9	5.8 5.9	5.9	5.9	8.7 8.0	8.4	10.1	
					Middle	3.2	19.5 19.5	19.5	8.1 8.1	8.1	27.7 27.6	27.7	87.8 90.0	88.9	6.9 7.0	6.9		6.0 5.8	5.9		9.6 9.3	9.5		
					Bottom	5.4	19.5 19.5	19.5	8.1 8.1	8.1	27.7 27.7	27.7	88.1 88.9	88.5	6.9 6.9	6.9		5.8 6.0	5.9		12.5 12.2	12.4		
30-Dec-15	Cloudy	Moderate	09:54	6.7	Surface	1.0	19.6 19.6	19.6	8.1 8.1	8.1	28.2 28.3	28.3	87.7 86.1	86.9	6.8 6.7	6.7	6.7	3.6 3.5	3.6	3.5	3.3 3.8	3.6	4.3	
					Middle	3.4	19.6 19.6	19.6	8.1 8.1	8.1	28.3 28.3	28.3	86.2 86.4	86.3	6.7 6.7	6.7		3.5 3.5	3.5		4.5 4.6	4.6		
					Bottom	5.7	19.6 19.6	19.6	8.1 8.1	8.1	28.3 28.2	28.3	86.0 86.3	86.2	6.7 6.7	6.7		3.4 3.5	3.5		4.6 5.0	4.8		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	18:41	5.2	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	27.2 27.4	27.3	87.4 86.4	86.9	6.3 6.2	6.3	6.3	2.6 2.6	2.6	2.6	2.4 3.3	2.9	3.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.2	23.9 23.9	23.9	8.1 8.1	8.1	28.6 28.7	28.6	86.9 86.3	86.6	6.2 6.2	6.2		6.2	2.6 2.6		2.6	6.2		2.6 2.6	2.6	3.2 2.8	3.0
4-Dec-15	Cloudy	Moderate	05:20	5.0	Surface	1.0	23.6 23.5	23.6	8.0 8.0	8.0	27.6 27.2	27.4	85.5 87.4	86.5	6.2 6.4	6.3	6.3	2.2 2.2	2.2	2.2	2.2 3.2	2.7	2.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	23.5 23.8	23.7	8.0 8.0	8.0	29.2 29.0	29.1	86.0 88.6	87.3	6.2 6.3	6.3		6.3	2.2 2.2		2.2	6.3		2.2 2.2	2.2	2.6 3.0	2.8
7-Dec-15	Cloudy	Moderate	09:16	5.0	Surface	1.0	22.8 22.9	22.9	8.1 8.1	8.1	29.8 30.0	29.9	88.3 87.6	88.0	6.4 6.3	6.4	6.4	3.4 3.6	3.5	3.5	2.5 3.9	3.2	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	22.8 22.9	22.9	8.1 8.1	8.1	29.6 29.9	29.8	88.9 87.8	88.4	6.5 6.4	6.4		6.4	3.5 3.5		3.5	6.4		3.5 3.5	3.5	2.6 4.3	3.5
9-Dec-15	Rainy	Moderate	10:46	5.2	Surface	1.0	22.3 22.3	22.3	8.1 8.1	8.1	30.9 31.0	31.0	87.6 86.2	86.9	6.4 6.3	6.3	6.3	3.2 3.2	3.2	3.2	4.5 4.0	4.3	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.2	22.3 22.4	22.4	8.1 8.1	8.1	31.0 30.7	30.8	86.9 88.8	87.9	6.3 6.5	6.4		6.4	3.3 3.1		3.2	6.4		3.3 3.1	3.2	4.4 4.1	4.3
11-Dec-15	Sunny	Moderate	13:55	4.6	Surface	1.0	22.0 21.9	21.9	8.2 8.2	8.2	31.2 31.2	31.2	85.9 85.6	85.8	6.3 6.3	6.3	6.3	4.5 4.9	4.7	4.8	4.3 4.1	4.2	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.6	21.9 21.9	21.9	8.2 8.2	8.2	31.3 31.3	31.3	85.6 85.6	85.6	6.3 6.3	6.3		6.3	4.8 5.0		4.9	6.3		4.8 5.0	4.9	4.3 4.0	4.2
14-Dec-15	Rainy	Moderate	16:00	5.3	Surface	1.0	21.7 21.6	21.6	8.2 8.2	8.2	28.7 28.9	28.8	87.6 88.4	88.0	6.5 6.6	6.6	6.6	3.8 3.9	3.9	3.9	4.5 3.8	4.2	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	21.6 21.8	21.7	8.2 8.2	8.2	29.1 30.1	29.6	88.2 88.0	88.1	6.6 6.5	6.5		6.5	3.9 3.8		3.9	6.5		3.9 3.8	3.9	5.2 4.2	4.7
16-Dec-15	Sunny	Moderate	17:37	5.3	Surface	1.0	21.0 21.1	21.1	8.2 8.2	8.2	27.9 27.9	27.9	88.5 88.1	88.3	6.7 6.7	6.7	6.7	4.5 4.2	4.4	4.3	7.5 6.8	7.2	7.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	21.2 21.2	21.2	8.2 8.2	8.2	29.2 29.6	29.4	89.1 86.8	88.0	6.7 6.5	6.6		6.6	4.2 4.2		4.2	6.6		4.2 4.2	4.2	6.0 7.5	6.8
18-Dec-15	Sunny	Moderate	13:55	5.2	Surface	1.0	20.2 20.3	20.3	8.2 8.2	8.2	30.6 30.7	30.7	86.8 86.8	86.8	6.6 6.6	6.6	6.6	3.8 3.9	3.9	3.9	6.8 6.3	6.6	6.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.2	20.2 20.4	20.3	8.2 8.2	8.2	30.7 30.9	30.8	87.0 87.0	87.0	6.6 6.5	6.6		6.6	3.9 3.9		3.9	6.6		3.9 3.9	3.9	6.5 6.4	6.5
21-Dec-15	Cloudy	Moderate	16:41	5.5	Surface	1.0	20.3 20.3	20.3	8.2 8.2	8.2	30.4 30.4	30.4	86.9 88.5	87.7	6.6 6.7	6.6	6.6	2.2 2.4	2.3	2.4	5.0 5.8	5.4	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.5	20.2 20.2	20.2	8.2 8.2	8.2	30.5 30.6	30.6	87.1 87.0	87.1	6.6 6.6	6.6		6.6	2.3 2.5		2.4	6.6		2.3 2.5	2.4	4.9 5.3	5.1

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-Dec-15	Sunny	Moderate	10:04	5.2	Surface	1.0	20.1 20.1	20.1	8.1 8.1	8.1	28.8 29.4	29.1	87.9 88.4	88.2	6.7 6.8	6.7	6.7	3.2 3.2	3.2	3.3	5.0 3.0	4.0	4.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.2	20.1 20.0	20.0	8.1 8.2	8.1	29.4 28.4	28.9	87.5 88.4	88.0	6.7 6.8	6.7		6.7	3.3 3.2		3.3	6.7		4.8 2.9	3.9	6.7
25-Dec-15	Cloudy	Moderate	13:50	5.0	Surface	1.0	20.2 20.2	20.2	8.2 8.2	8.2	27.5 27.4	27.4	90.1 88.2	89.2	7.0 6.8	6.9	6.9	4.8 4.8	4.8	4.8	5.5 7.1	6.3	5.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.0	20.2 20.2	20.2	8.1 8.2	8.2	28.9 29.0	29.0	89.6 88.9	89.3	6.8 6.8	6.8		6.8	4.8 4.7		4.8	6.8		4.8 4.7	4.8	6.8
28-Dec-15	Sunny	Moderate	15:40	4.9	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	28.7 28.6	28.7	89.9 90.6	90.3	6.9 7.0	7.0	7.0	4.1 4.2	4.2	4.2	6.0 5.0	5.5	7.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.9	19.7 19.7	19.7	8.2 8.2	8.2	28.8 29.0	28.9	89.4 86.7	88.1	6.9 6.7	6.8		6.8	4.2 4.0		4.1	6.8		4.2 4.0	4.1	6.8
30-Dec-15	Cloudy	Moderate	17:03	4.8	Surface	1.0	19.7 19.7	19.7	8.2 8.2	8.2	29.0 29.0	29.0	90.3 88.1	89.2	7.0 6.8	6.9	6.9	3.2 3.4	3.3	3.6	2.4 3.3	2.9	2.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.8	19.7 19.6	19.7	8.2 8.2	8.2	29.2 29.3	29.2	88.6 87.9	88.3	6.8 6.8	6.8		6.8	3.8 4.0		3.9	6.8		3.8 4.0	3.9	6.8

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-Dec-15	Sunny	Moderate	11:20	5.1	Surface	1.0	23.7 23.7	23.7	8.0 7.9	8.0	25.5 25.3	25.4	84.4 84.3	84.4	6.2 6.2	6.2	6.2	3.8 3.9	3.9	3.9	4.1 4.7	4.4	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	23.8 23.8	23.8	7.8 8.0	7.9	26.2 26.8	26.5	85.0 84.1	84.6	6.2 6.1	6.1		6.1	3.8 4.0		3.9	6.1		3.7 4.3	4.0	6.1	
4-Dec-15	Cloudy	Moderate	15:21	5.3	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	28.1 28.2	28.2	86.5 84.1	85.3	6.3 6.1	6.2	6.2	2.2 2.2	2.2	2.3	2.8 2.7	2.8	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	23.8 23.5	23.7	8.1 8.1	8.1	30.1 30.1	30.1	83.9 85.0	84.5	6.0 6.1	6.0		6.0	2.3 2.2		2.3	6.0		2.7 2.5	2.6	6.0	
7-Dec-15	Cloudy	Moderate	17:21	5.2	Surface	1.0	22.6 22.6	22.6	8.2 8.2	8.2	30.8 30.8	30.8	92.1 89.7	90.9	6.7 6.5	6.6	6.6	2.2 2.3	2.3	2.3	2.9 2.9	2.9	3.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.2	22.7 22.8	22.7	8.2 8.2	8.2	31.4 31.6	31.5	89.7 90.6	90.2	6.5 6.5	6.5		6.5	2.3 2.3		2.3	6.5		3.2 2.8	3.0	6.5	
9-Dec-15	Rainy	Moderate	18:10	5.3	Surface	1.0	22.3 22.3	22.3	8.2 8.2	8.2	31.2 31.2	31.2	84.8 84.8	84.8	6.2 6.2	6.2	6.2	6.5 6.4	6.5	6.5	4.6 4.2	4.4	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	22.3 22.3	22.3	8.2 8.2	8.2	31.2 31.2	31.2	85.0 84.9	85.0	6.2 6.2	6.2		6.2	6.4 6.5		6.5	6.2		5.7 6.5	6.1	6.2	
11-Dec-15	Sunny	Moderate	06:12	4.9	Surface	1.0	22.0 22.0	22.0	8.0 7.9	8.0	29.6 29.2	29.4	85.9 88.5	87.2	6.3 6.5	6.4	6.4	6.6 6.6	6.6	6.5	6.6 6.6	6.6	8.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.9	22.0 22.0	22.0	7.9 8.0	7.9	28.4 29.4	28.9	94.0 86.9	90.5	7.0 6.4	6.7		6.7	6.1 6.5		6.3	6.7		9.0 9.6	9.3	6.7	
14-Dec-15	Rainy	Moderate	08:31	5.0	Surface	1.0	21.7 21.7	21.7	8.0 8.0	8.0	28.3 28.2	28.3	86.8 86.4	86.6	6.5 6.5	6.5	6.5	6.1 6.3	6.2	6.2	11.1 9.5	10.3	10.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.0	21.7 21.7	21.7	8.0 8.0	8.0	28.3 28.1	28.2	86.3 86.5	86.4	6.4 6.5	6.5		6.5	6.1 6.1		6.1	6.5		10.6 11.3	11.0	6.5	
16-Dec-15	Sunny	Moderate	10:03	5.0	Surface	1.0	21.3 21.3	21.3	7.9 7.9	7.9	27.2 27.5	27.4	90.6 90.6	90.6	6.9 6.9	6.9	6.9	4.7 4.5	4.6	4.7	7.8 8.3	8.1	7.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.0	21.3 21.3	21.3	7.9 7.9	7.9	27.4 26.2	26.8	89.9 88.5	89.2	6.8 6.7	6.7		6.7	4.5 4.8		4.7	6.7		7.8 6.4	7.1	6.7	
18-Dec-15	Cloudy	Moderate	04:15	5.4	Surface	1.0	19.8 19.9	19.9	8.1 8.1	8.1	28.5 28.9	28.7	87.5 88.4	88.0	6.8 6.8	6.8	6.8	6.9 6.7	6.8	6.8	2.2 2.2	2.2	2.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.4	20.0 20.1	20.1	8.1 8.1	8.1	29.1 28.5	28.8	88.0 89.0	88.5	6.7 6.8	6.8		6.8	6.7 6.7		6.7	6.8		2.3 2.0	2.2	6.8	
21-Dec-15	Sunny	Moderate	07:44	5.3	Surface	1.0	20.2 20.2	20.2	8.0 8.0	8.0	28.8 29.3	29.1	91.1 88.6	89.9	7.0 6.8	6.9	6.9	2.7 3.0	2.9	3.1	4.4 2.5	3.5	3.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	20.2 20.2	20.2	8.0 8.0	8.0	29.2 28.3	28.8	85.7 91.0	88.4	6.5 7.0	6.8		6.8	3.2 3.3		3.3	6.8		3.4 4.3	3.9	6.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-Dec-15	Sunny	Moderate	17:45	5.3	Surface	1.0	20.1 20.1	20.1	8.2 8.2	8.2	28.3 28.3	28.3	90.7 91.9	91.3	7.0 7.1	7.0	7.0	3.4 3.3	3.4	3.4	3.6 3.4	3.5	3.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	20.1 20.1	20.1	8.2 8.2	8.2	29.9 30.5	30.2	89.8 90.7	90.3	6.8 6.9	6.9		3.4 3.4	3.4		3.5 2.5	3.0		3.0	3.0		
25-Dec-15	Cloudy	Moderate	06:43	5.0	Surface	1.0	20.2 20.2	20.2	8.1 8.1	8.1	26.5 26.4	26.5	88.5 87.5	88.0	6.9 6.8	6.8	6.8	8.1 7.8	8.0	7.9	8.0 8.9	8.5	8.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.0	20.3 20.2	20.3	8.1 8.1	8.1	27.6 28.1	27.8	88.2 87.2	87.7	6.8 6.7	6.7		7.8 7.6	7.7		9.3 8.5	8.9		8.9			
28-Dec-15	Sunny	Moderate	08:21	5.2	Surface	1.0	19.5 19.5	19.5	8.2 8.2	8.2	27.5 27.3	27.4	90.3 89.7	90.0	7.1 7.0	7.0	7.0	5.9 6.1	6.0	6.1	8.6 8.5	8.6	9.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.2	19.5 19.5	19.5	8.2 8.2	8.2	27.1 27.4	27.3	90.8 91.0	90.9	7.1 7.1	7.1		6.1 6.3	6.2		10.3 9.8	10.1		10.1			
30-Dec-15	Cloudy	Moderate	09:41	5.0	Surface	1.0	19.6 19.6	19.6	8.1 8.1	8.1	27.7 27.2	27.5	89.5 92.1	90.8	7.0 7.2	7.1	7.1	3.6 3.5	3.6	3.7	6.0 5.3	5.7	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	4.0	19.6 19.6	19.6	8.1 8.1	8.1	26.9 27.6	27.3	94.4 89.6	92.0	7.4 7.0	7.2		3.7 3.6	3.7		3.9 4.9	4.4		4.4			

Remarks:




Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

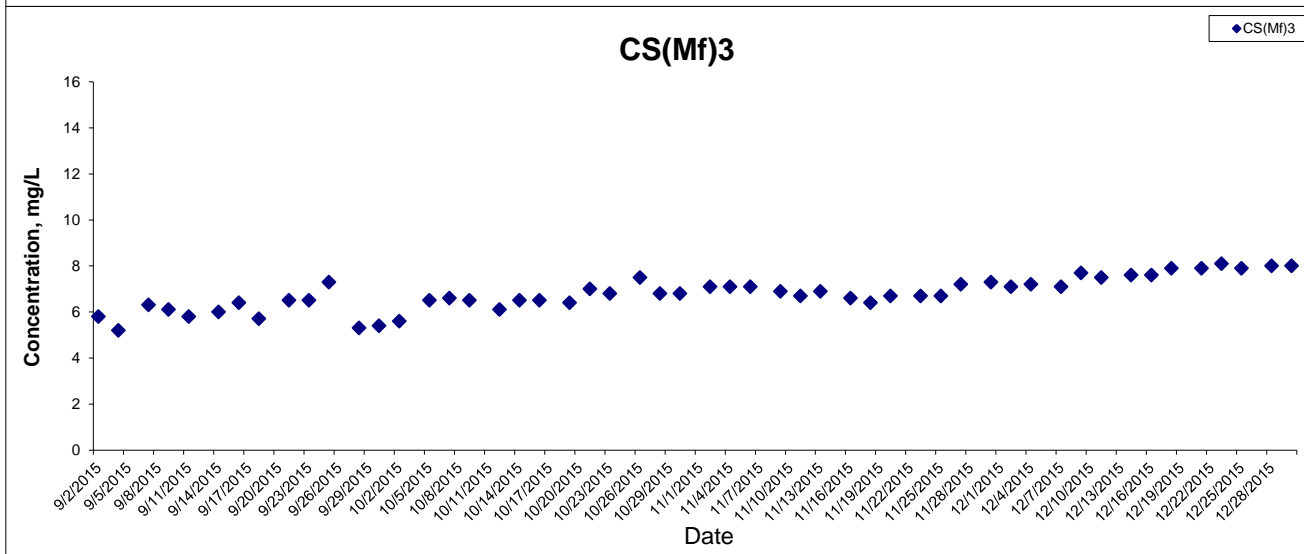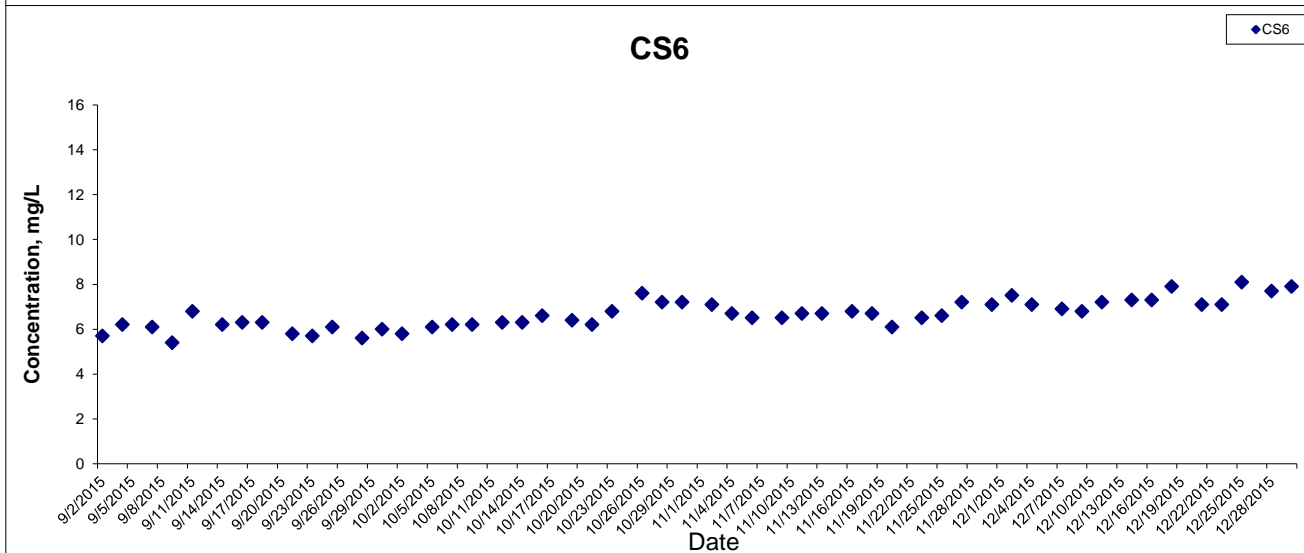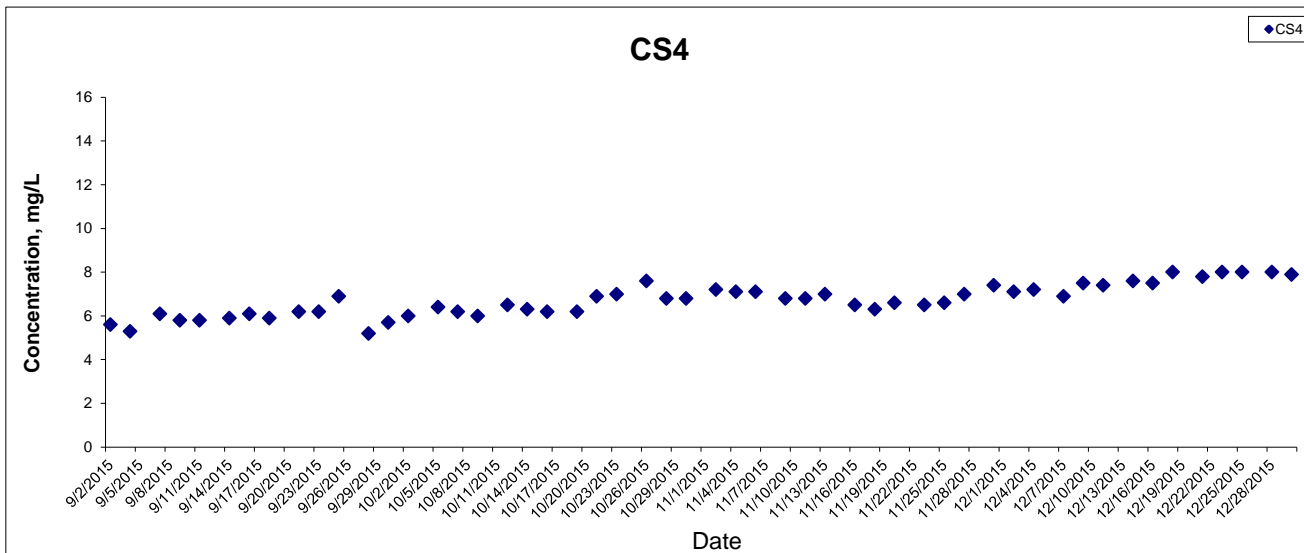




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results



Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

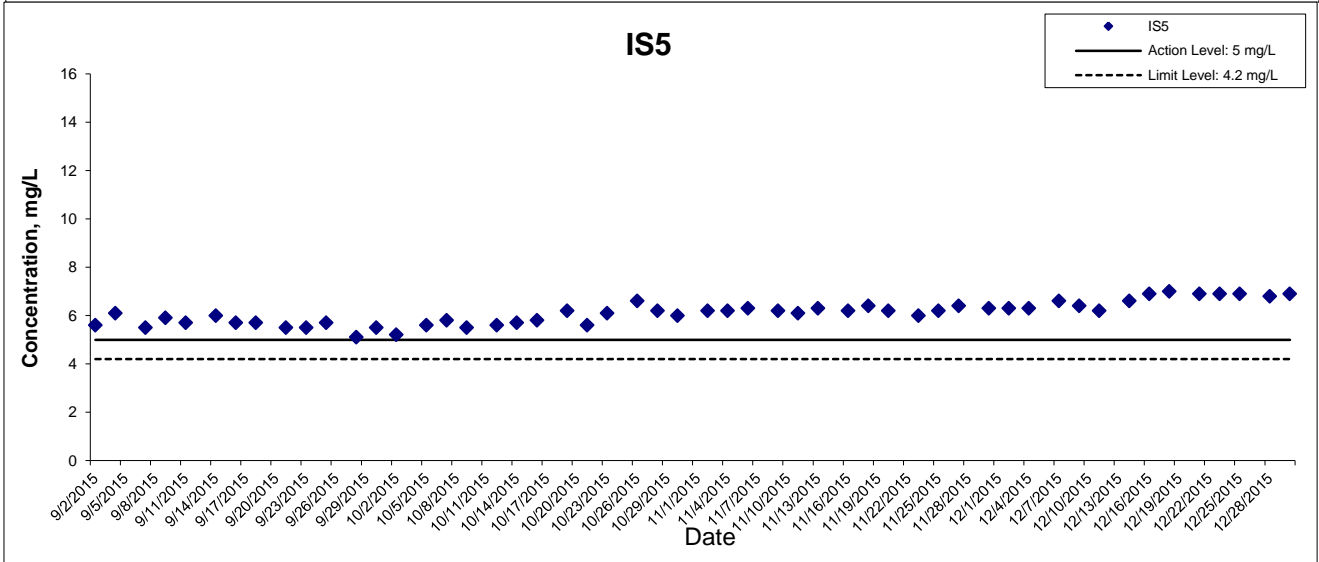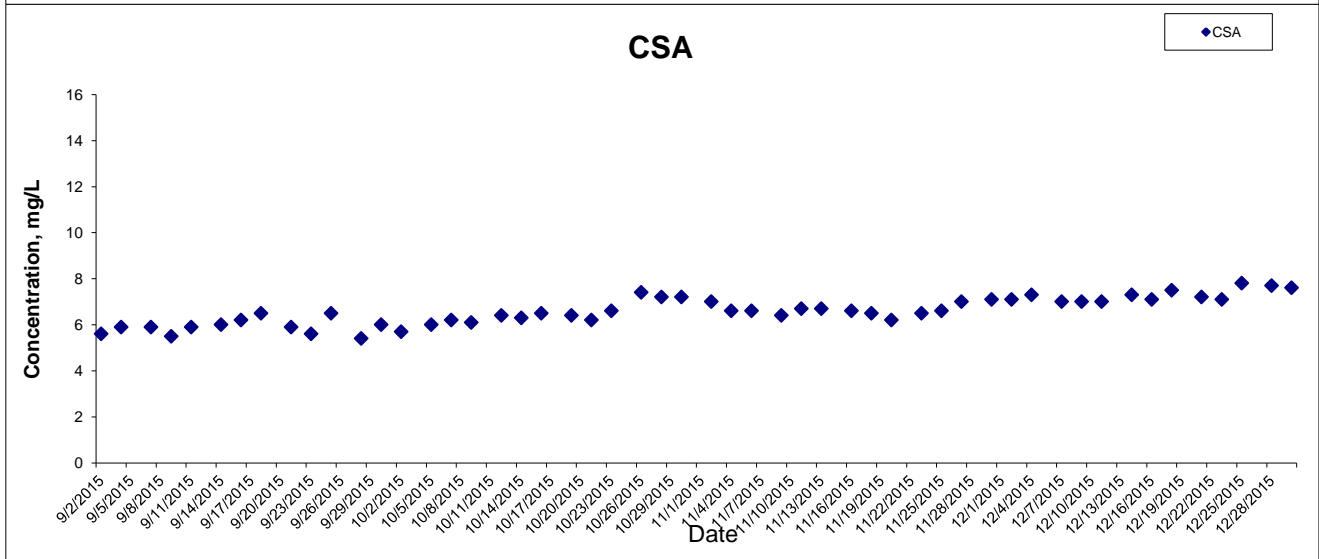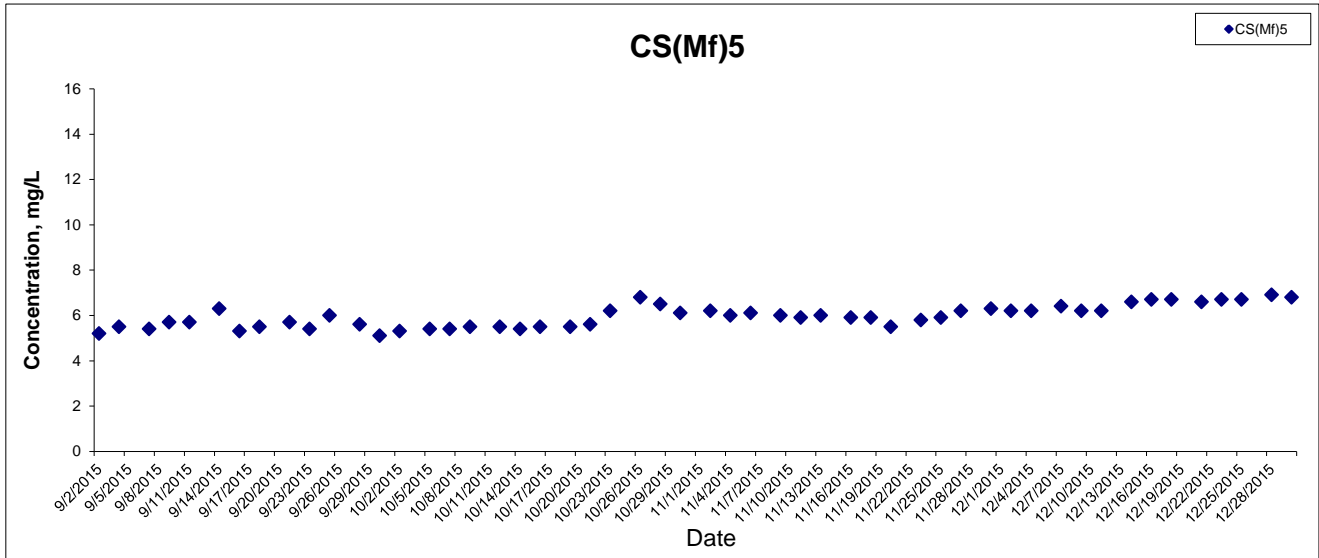




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results



Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

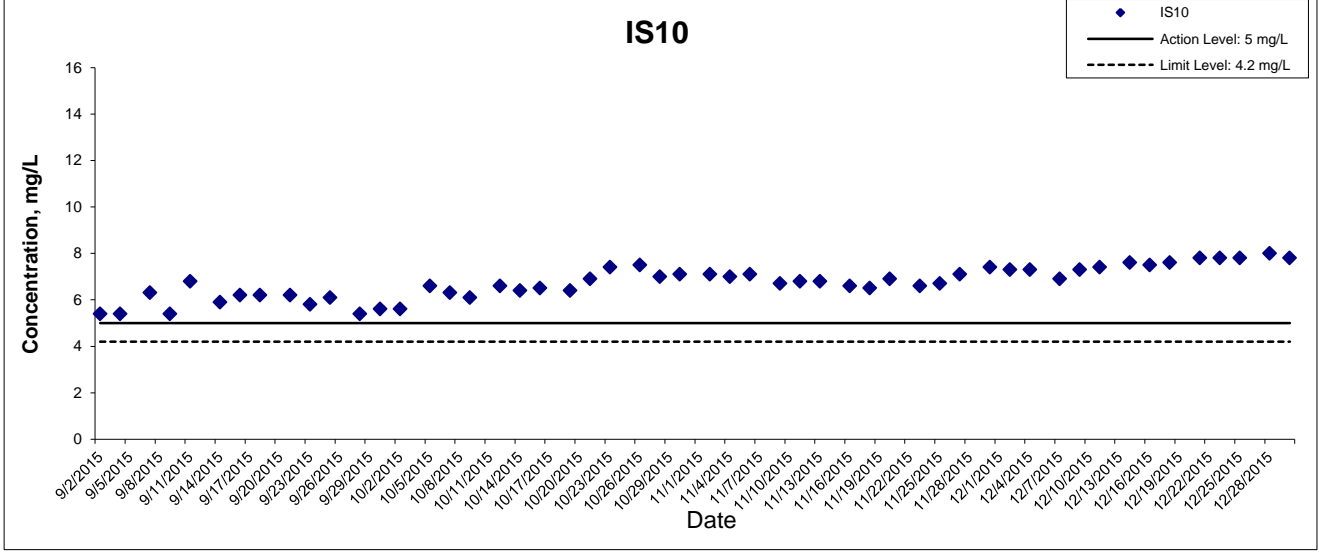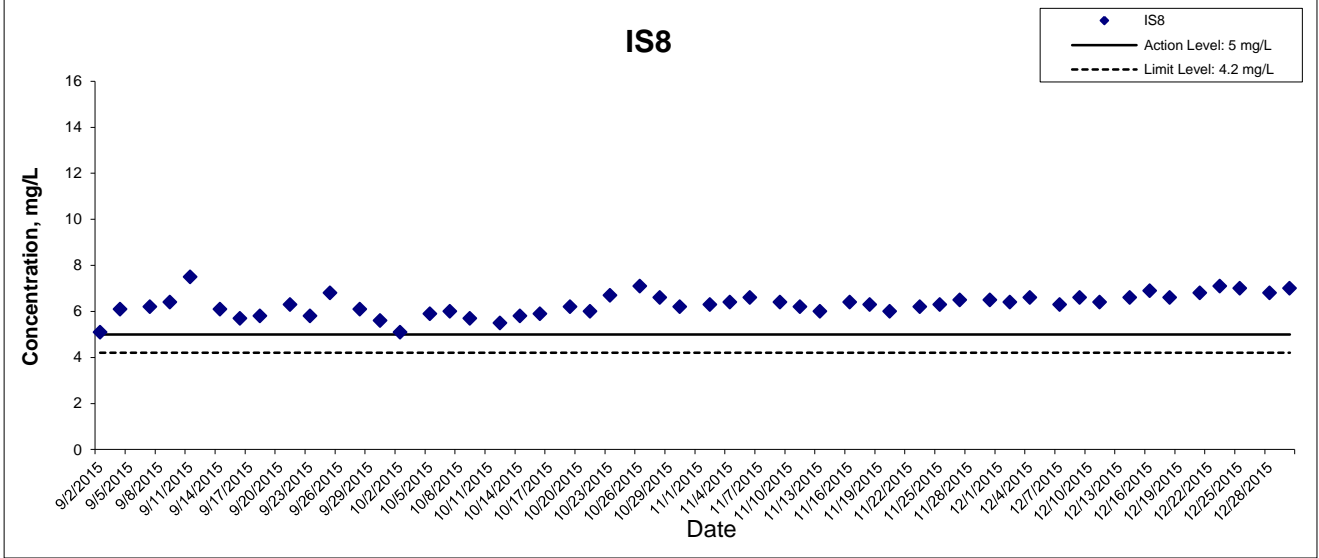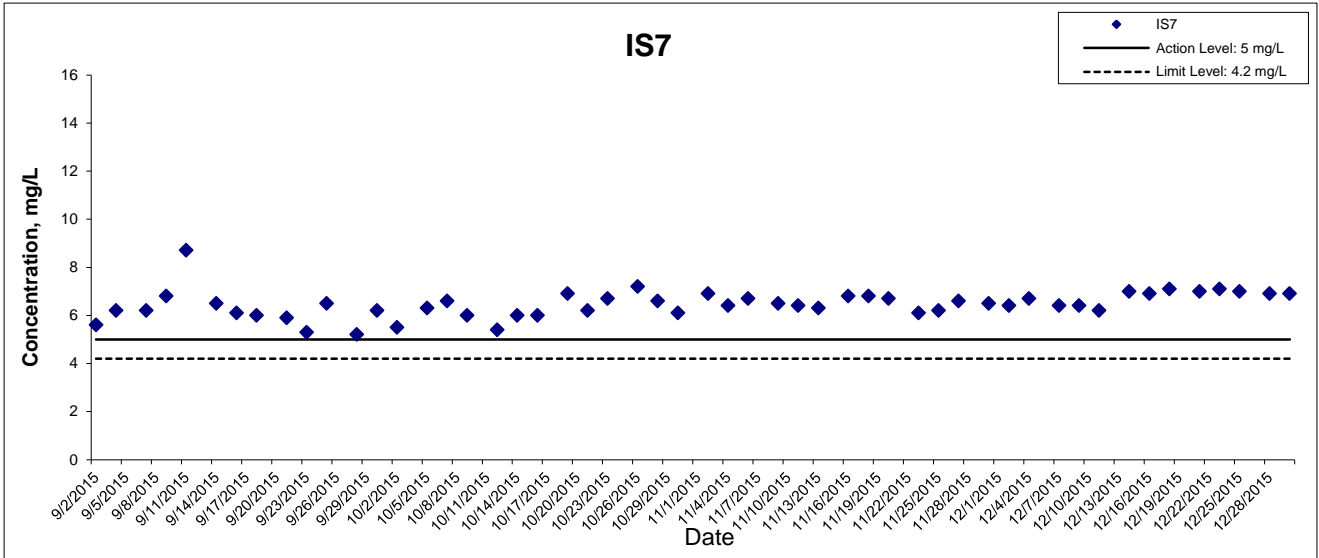




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results



Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

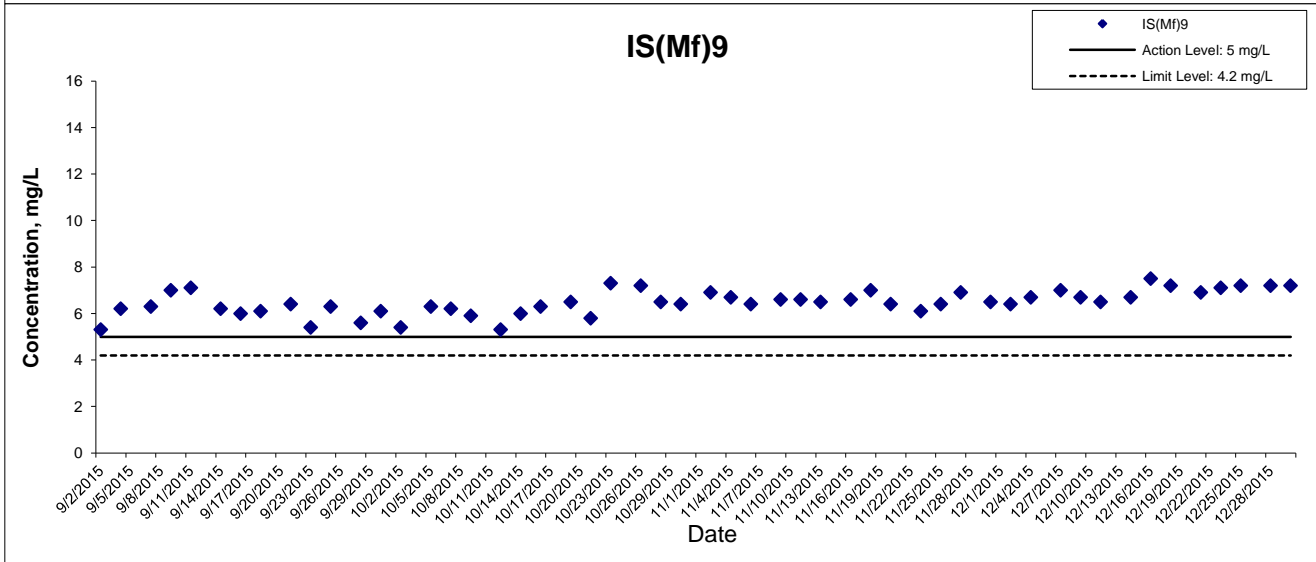
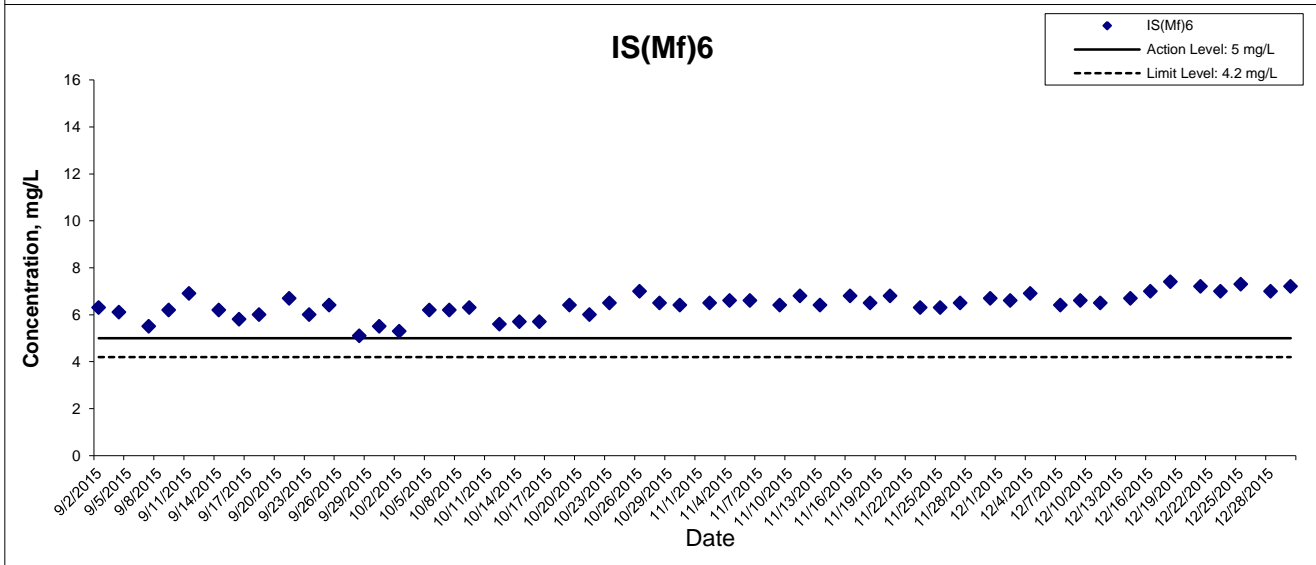
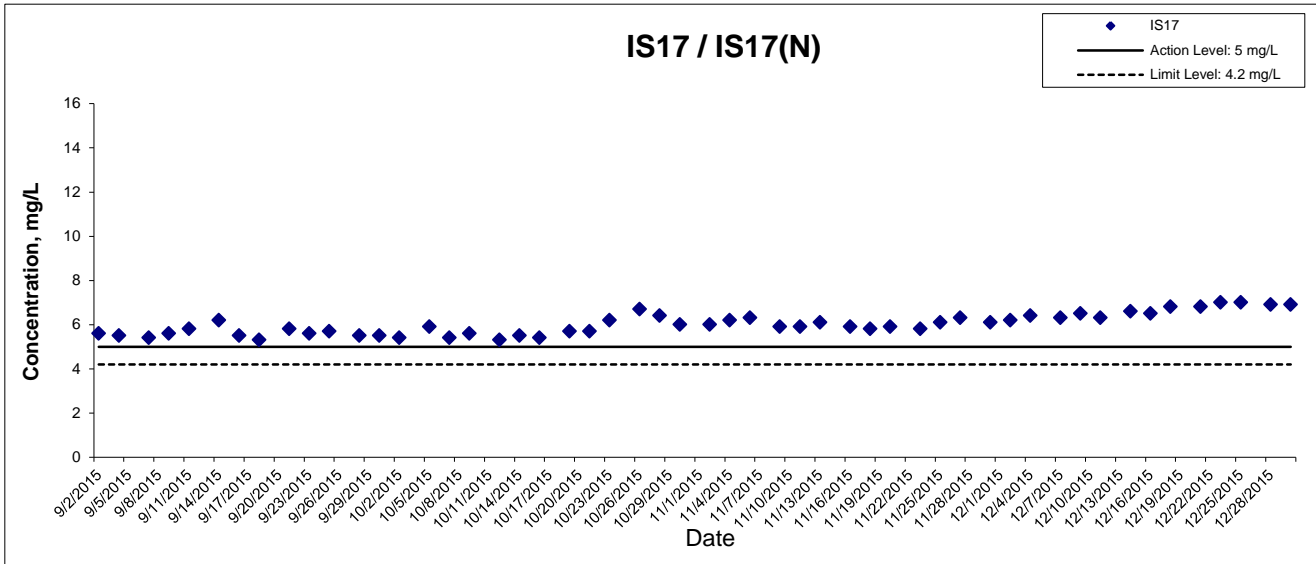


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

**HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS**

**Graphical Presentation of Impact Water Quality
 Monitoring Results**



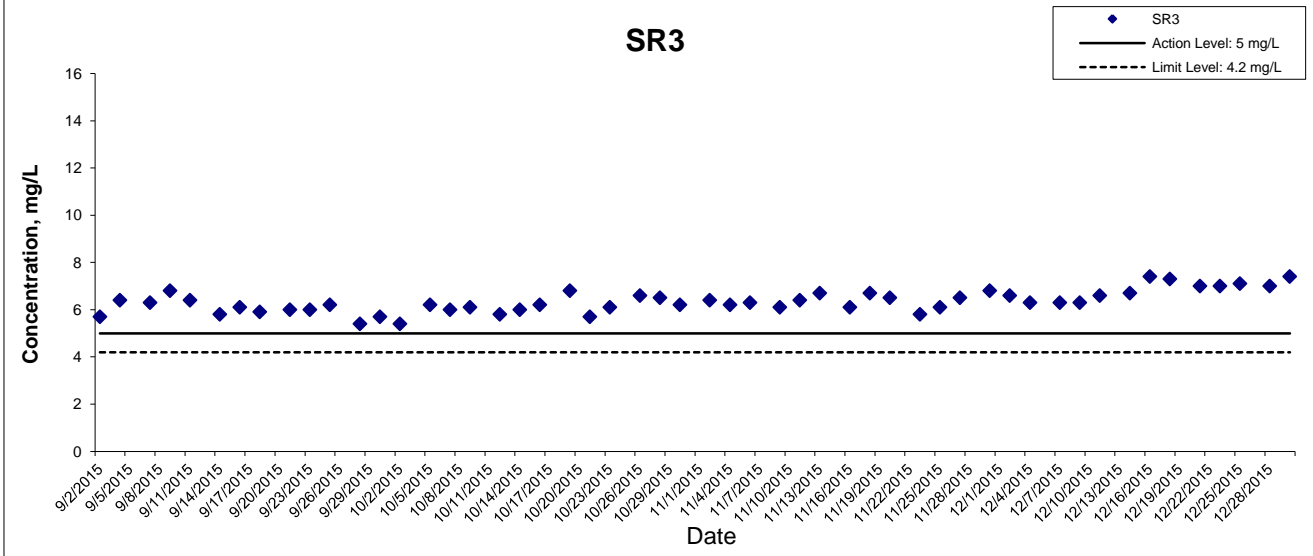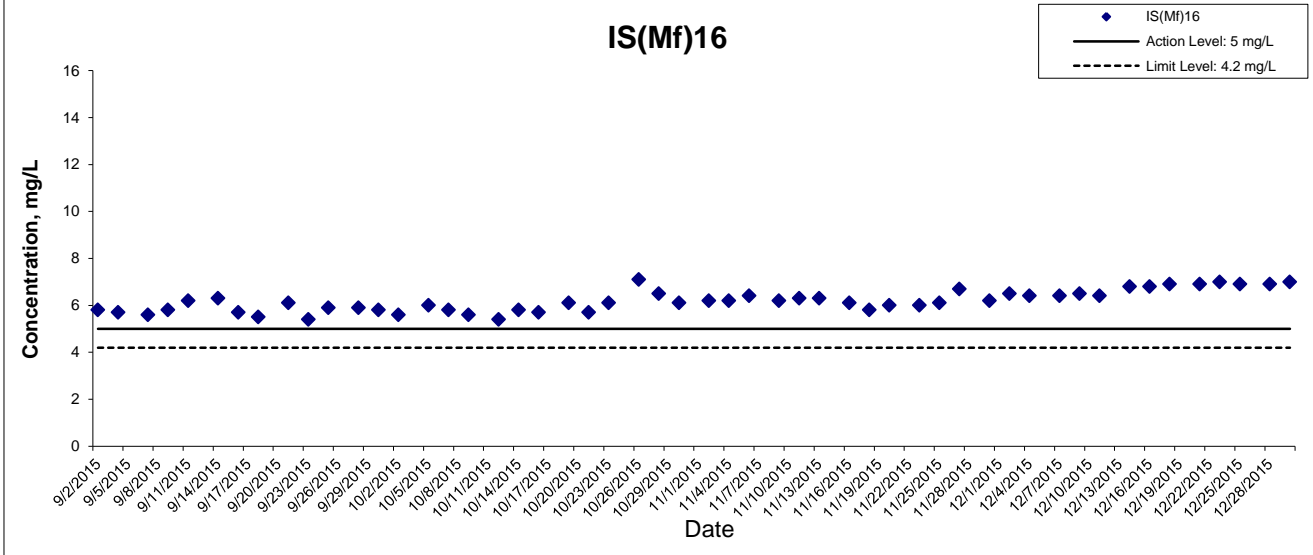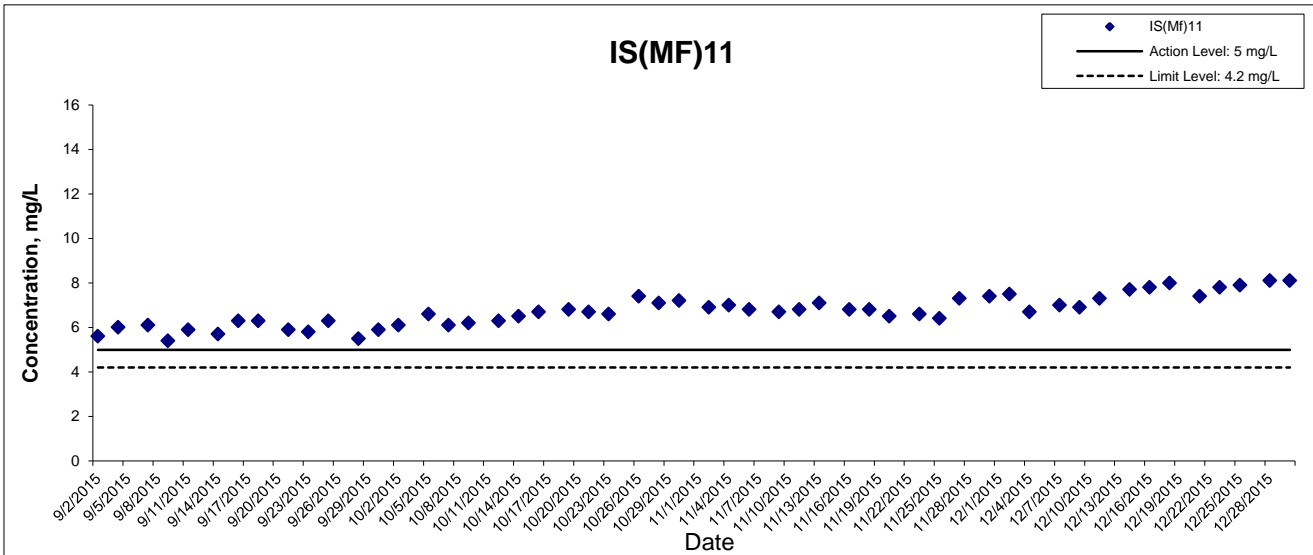

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS






**Graphical Presentation of Impact Water Quality
 Monitoring Results**

Project No.: 60249820




Date: January 2016

Appendix J

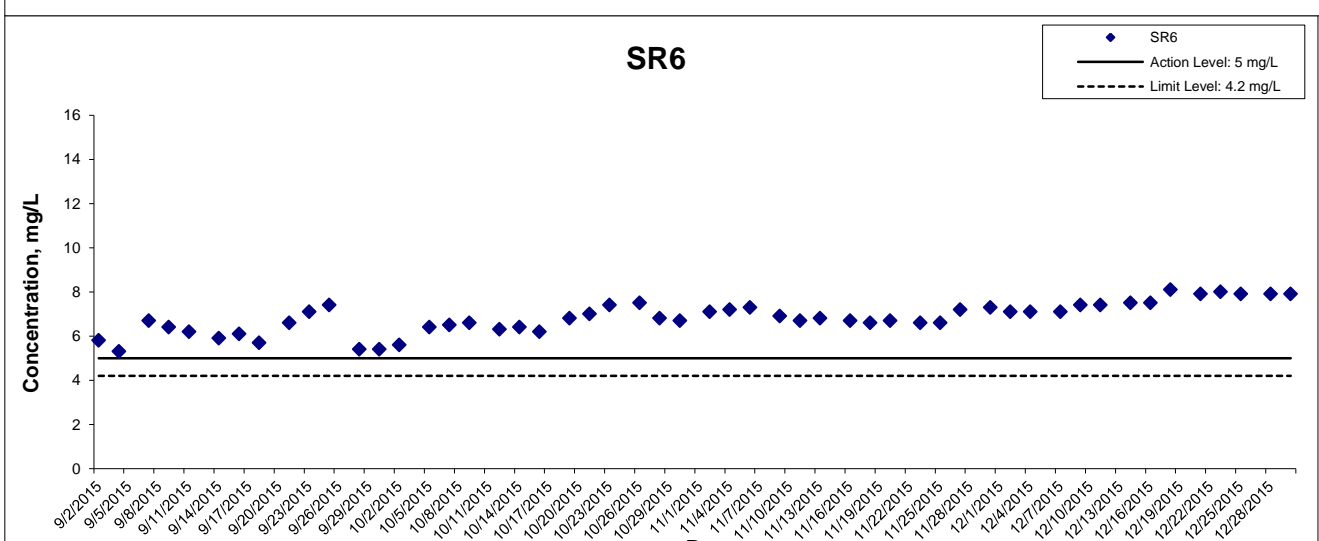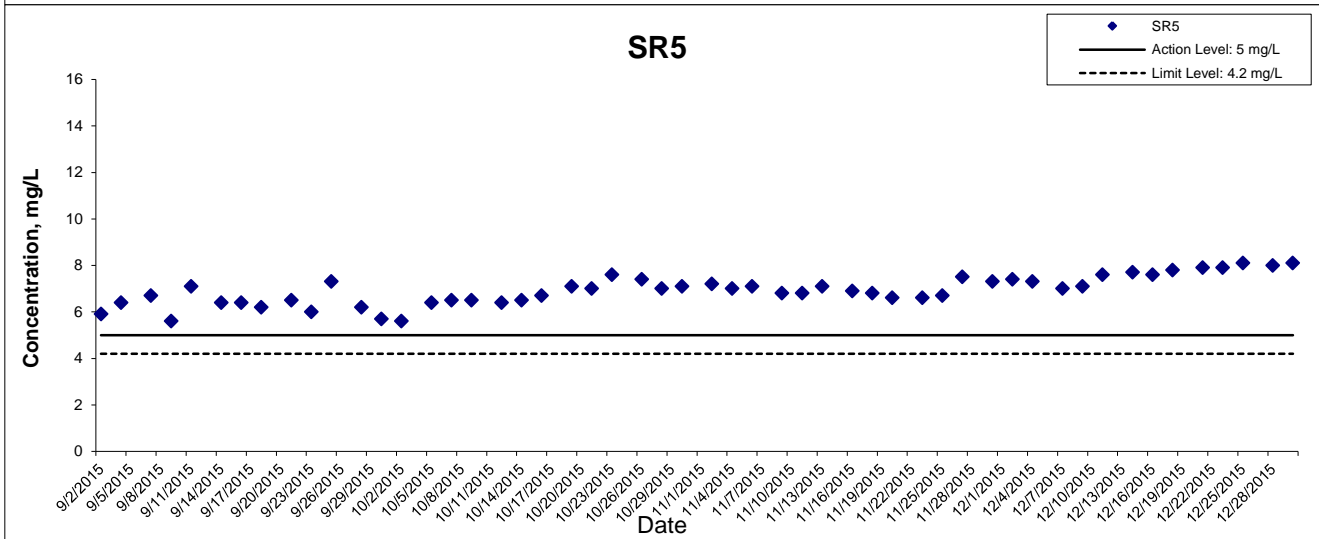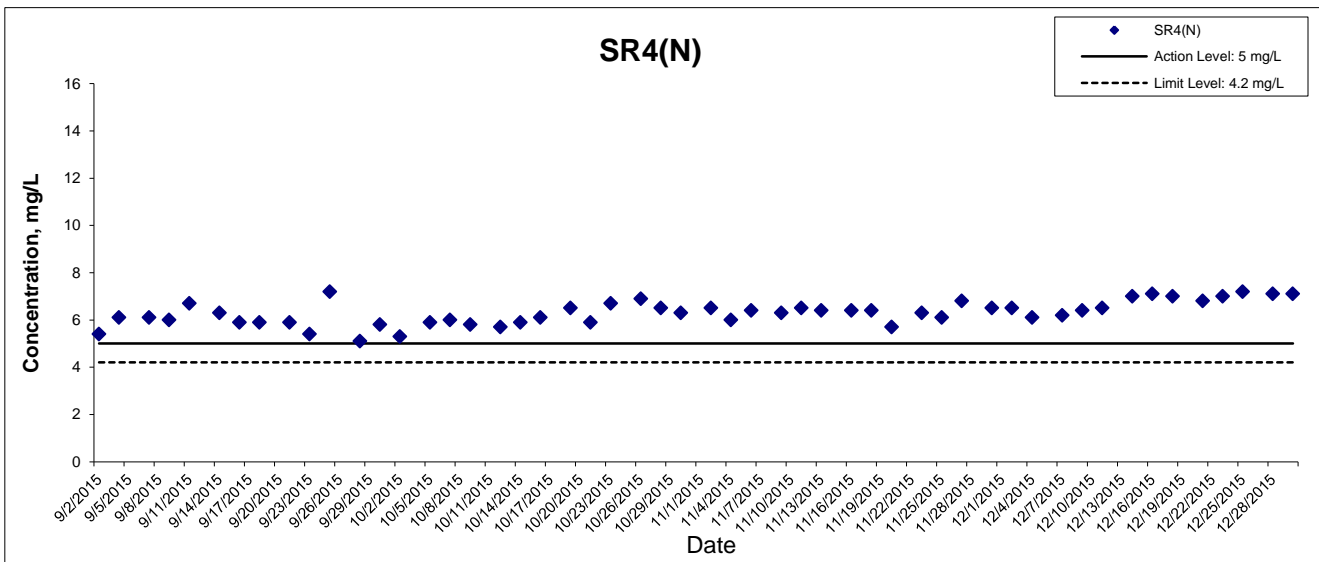


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.



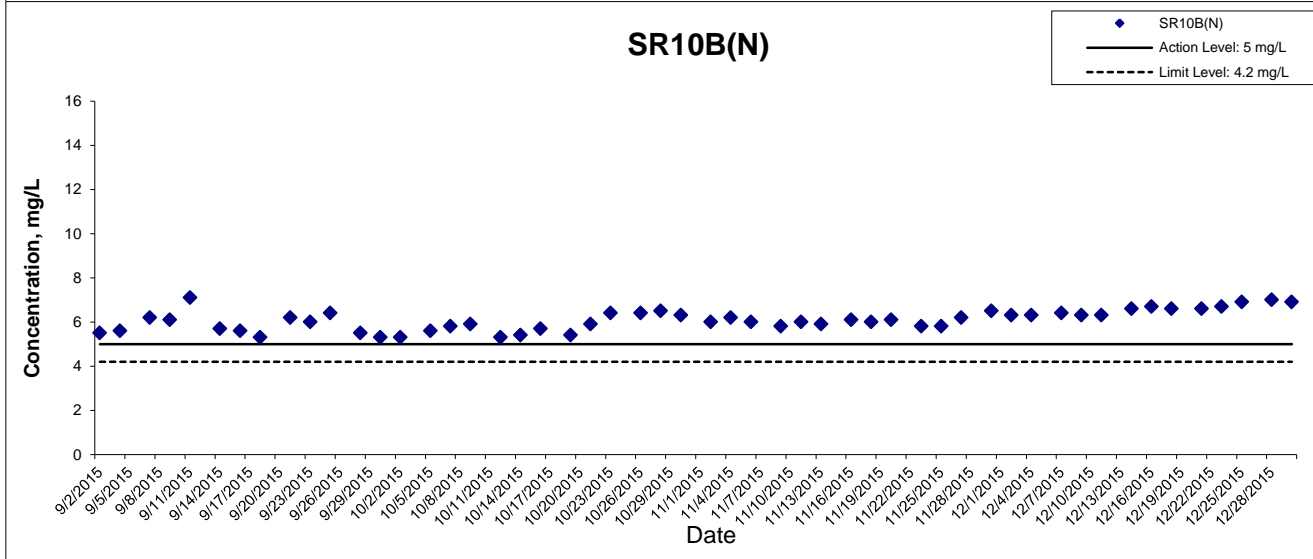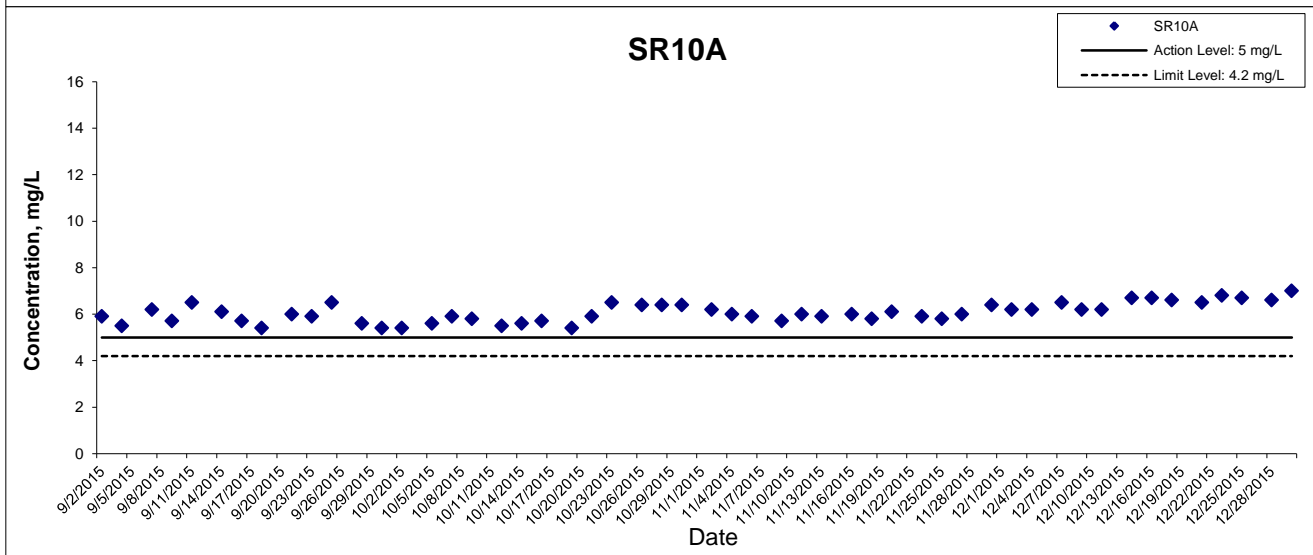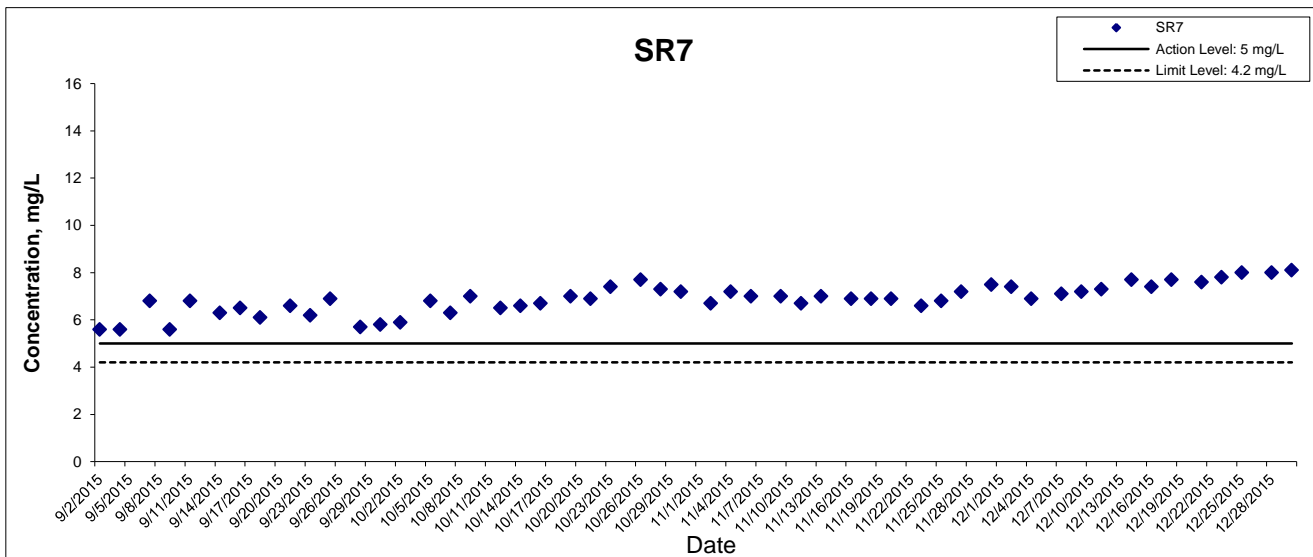

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

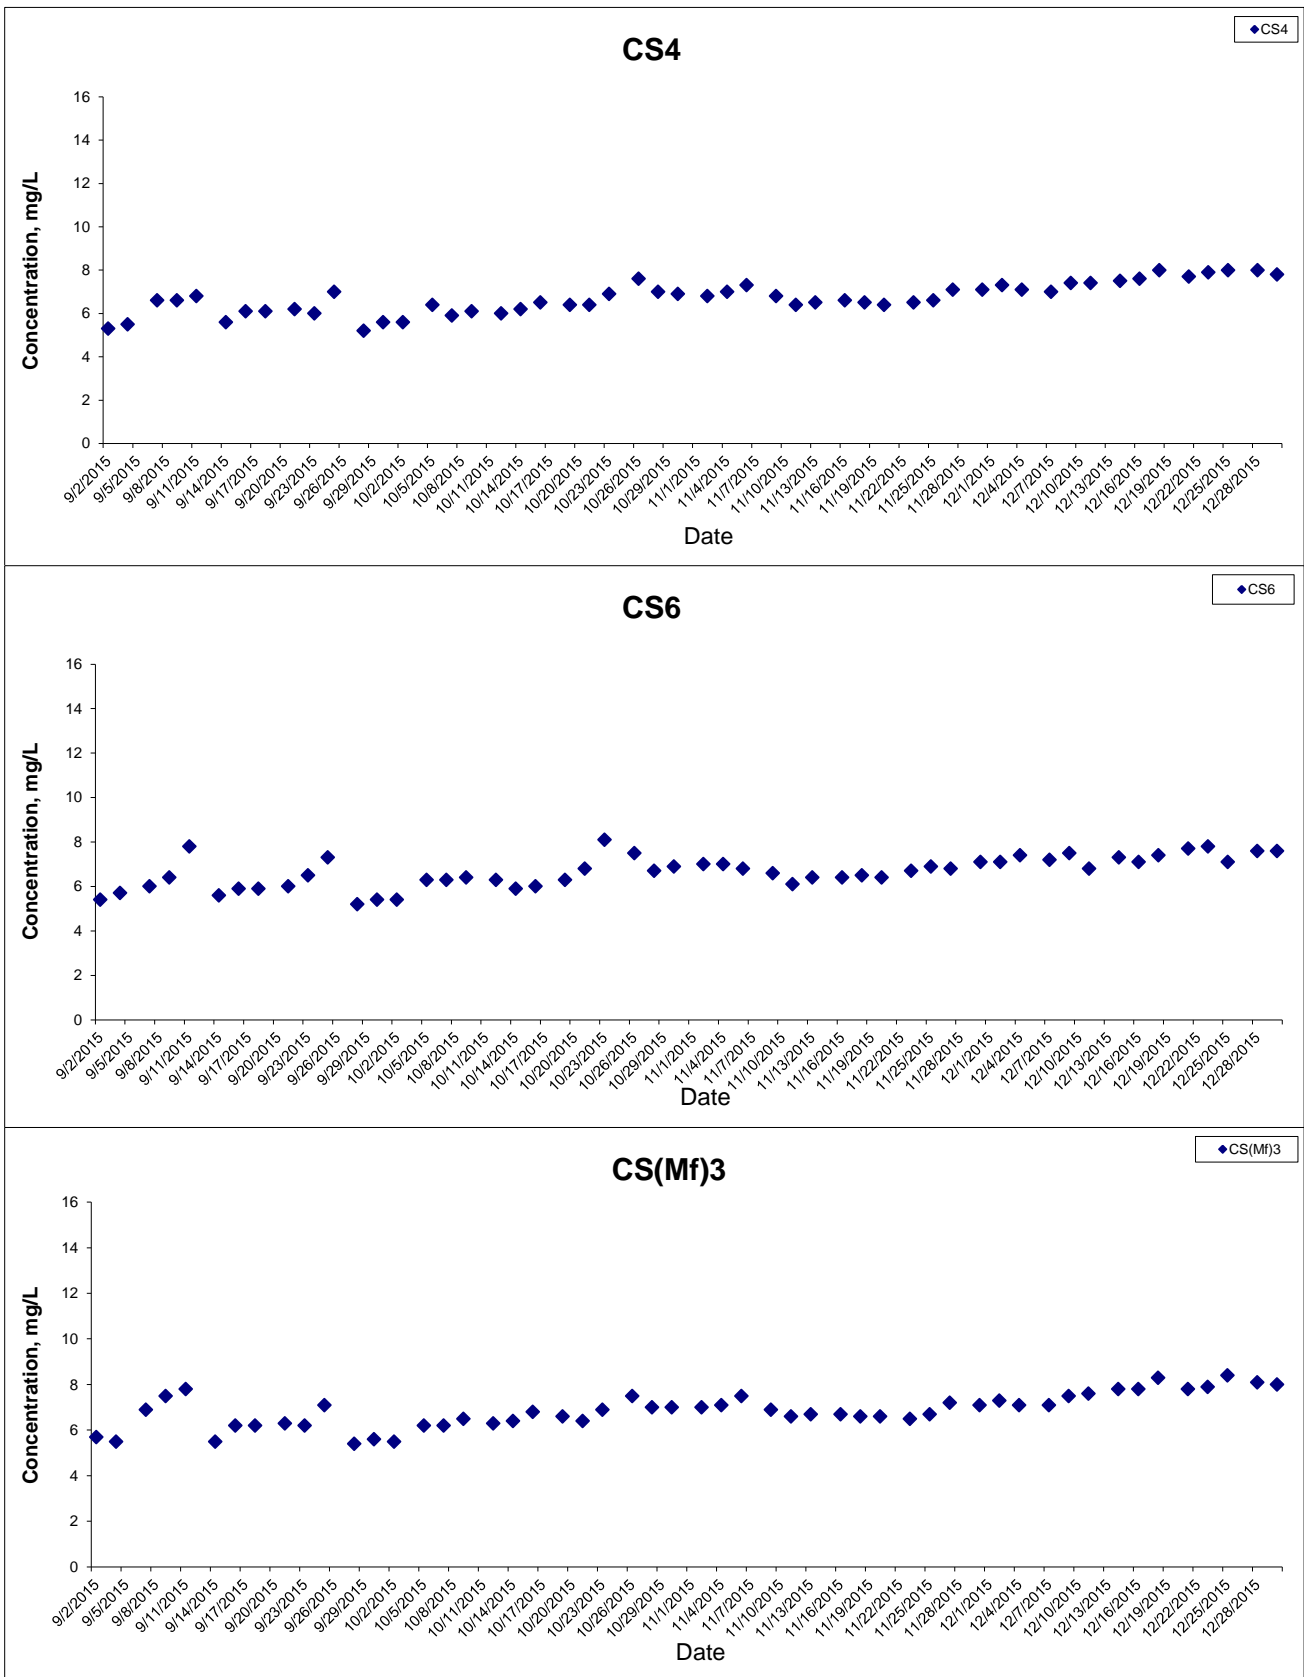


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results



Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

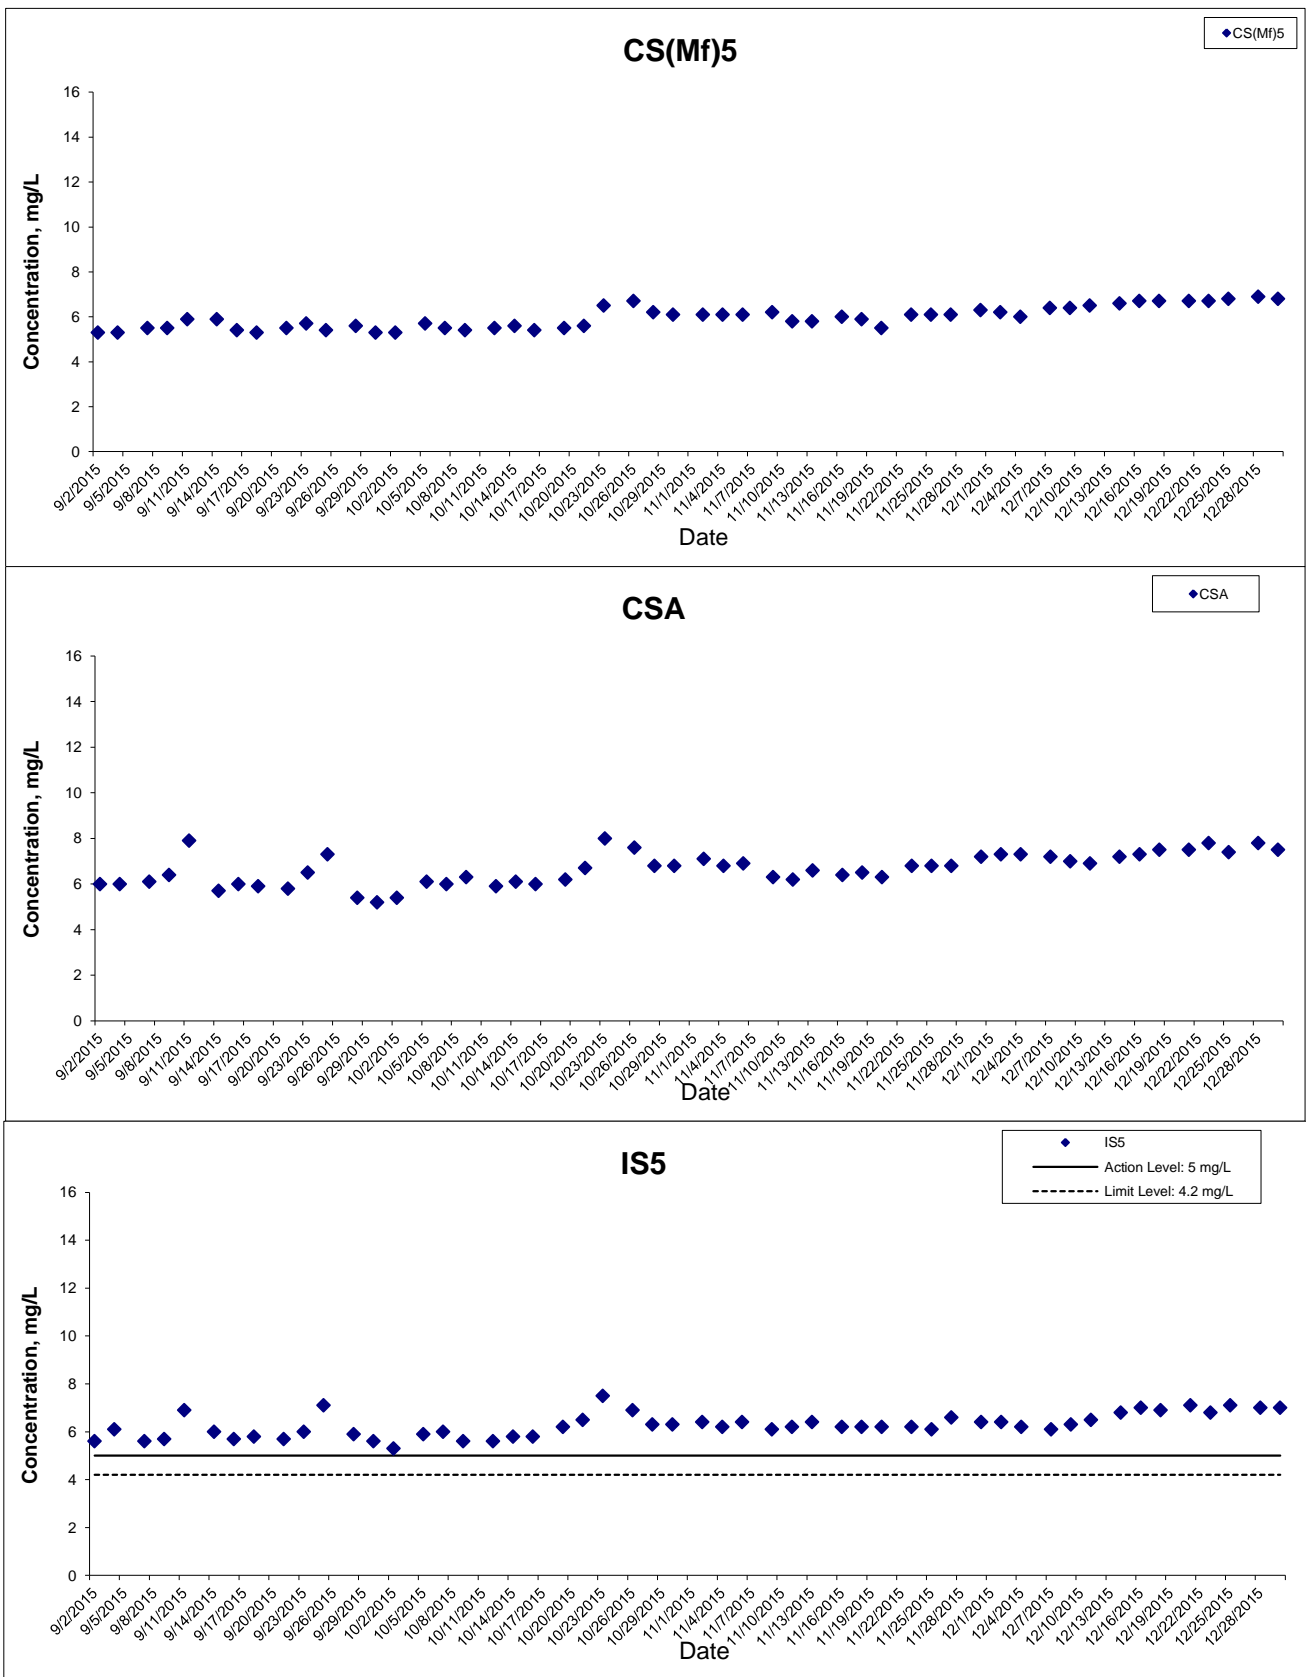




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results



Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

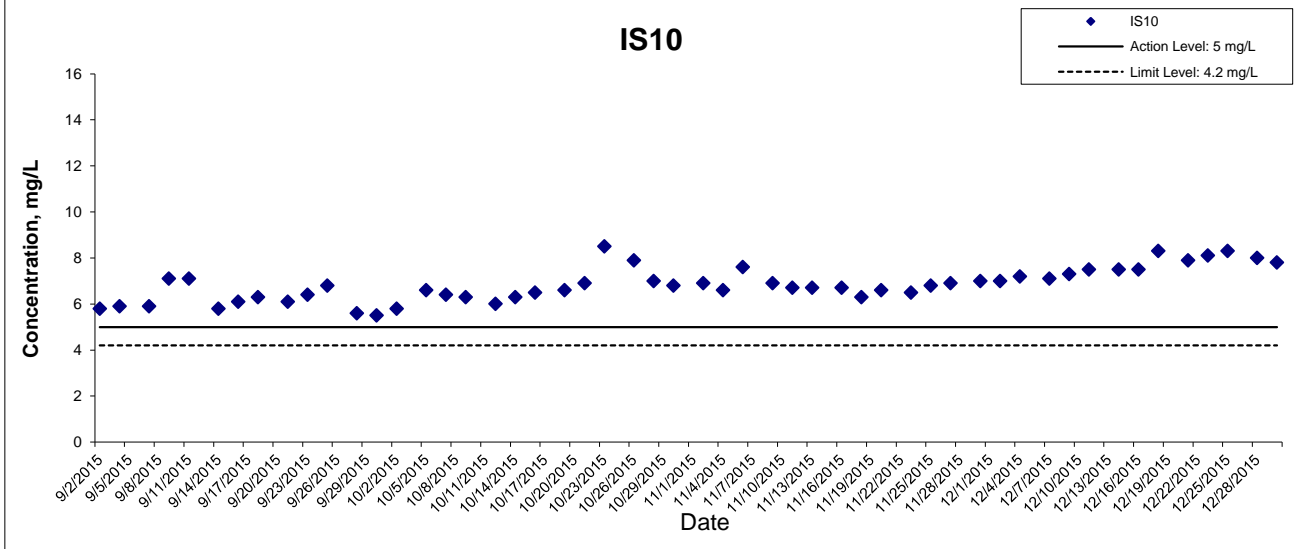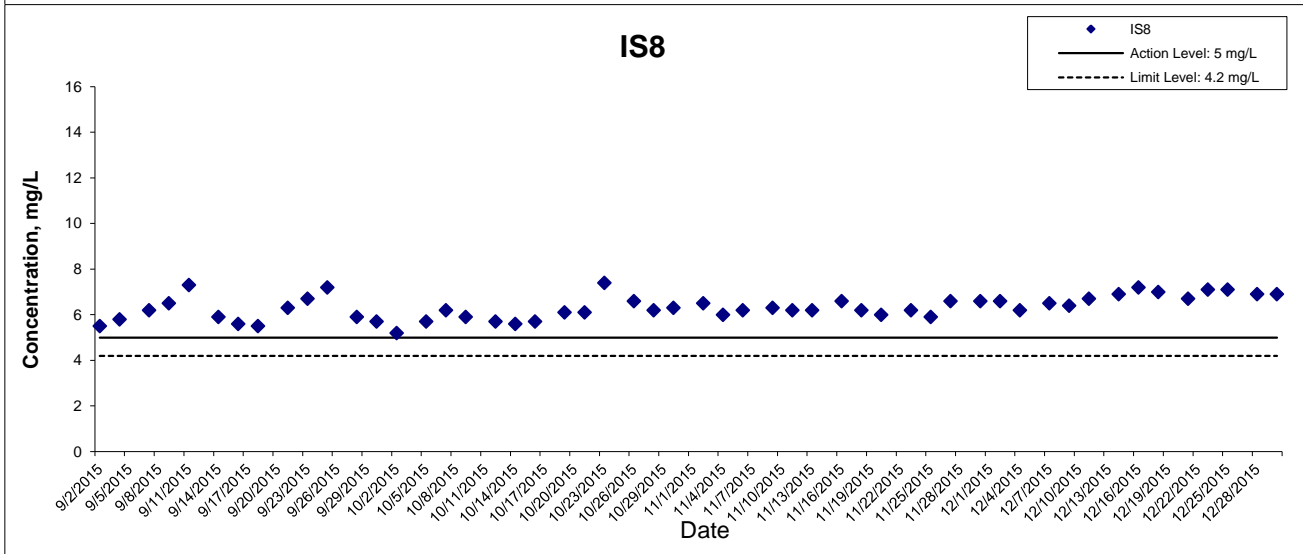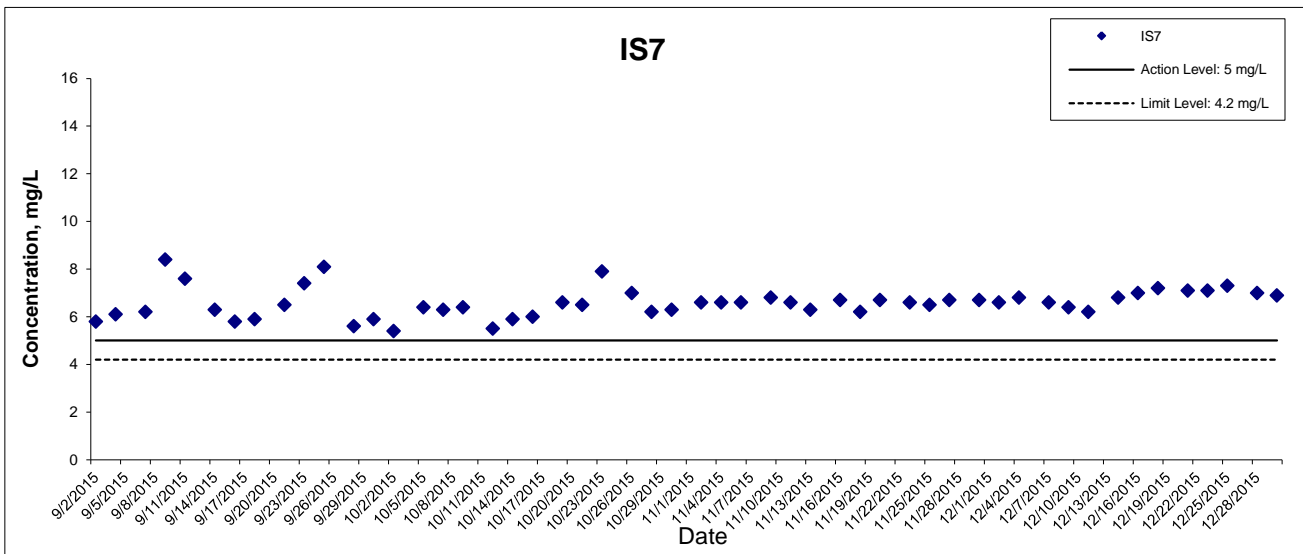


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
 Monitoring Results**






Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

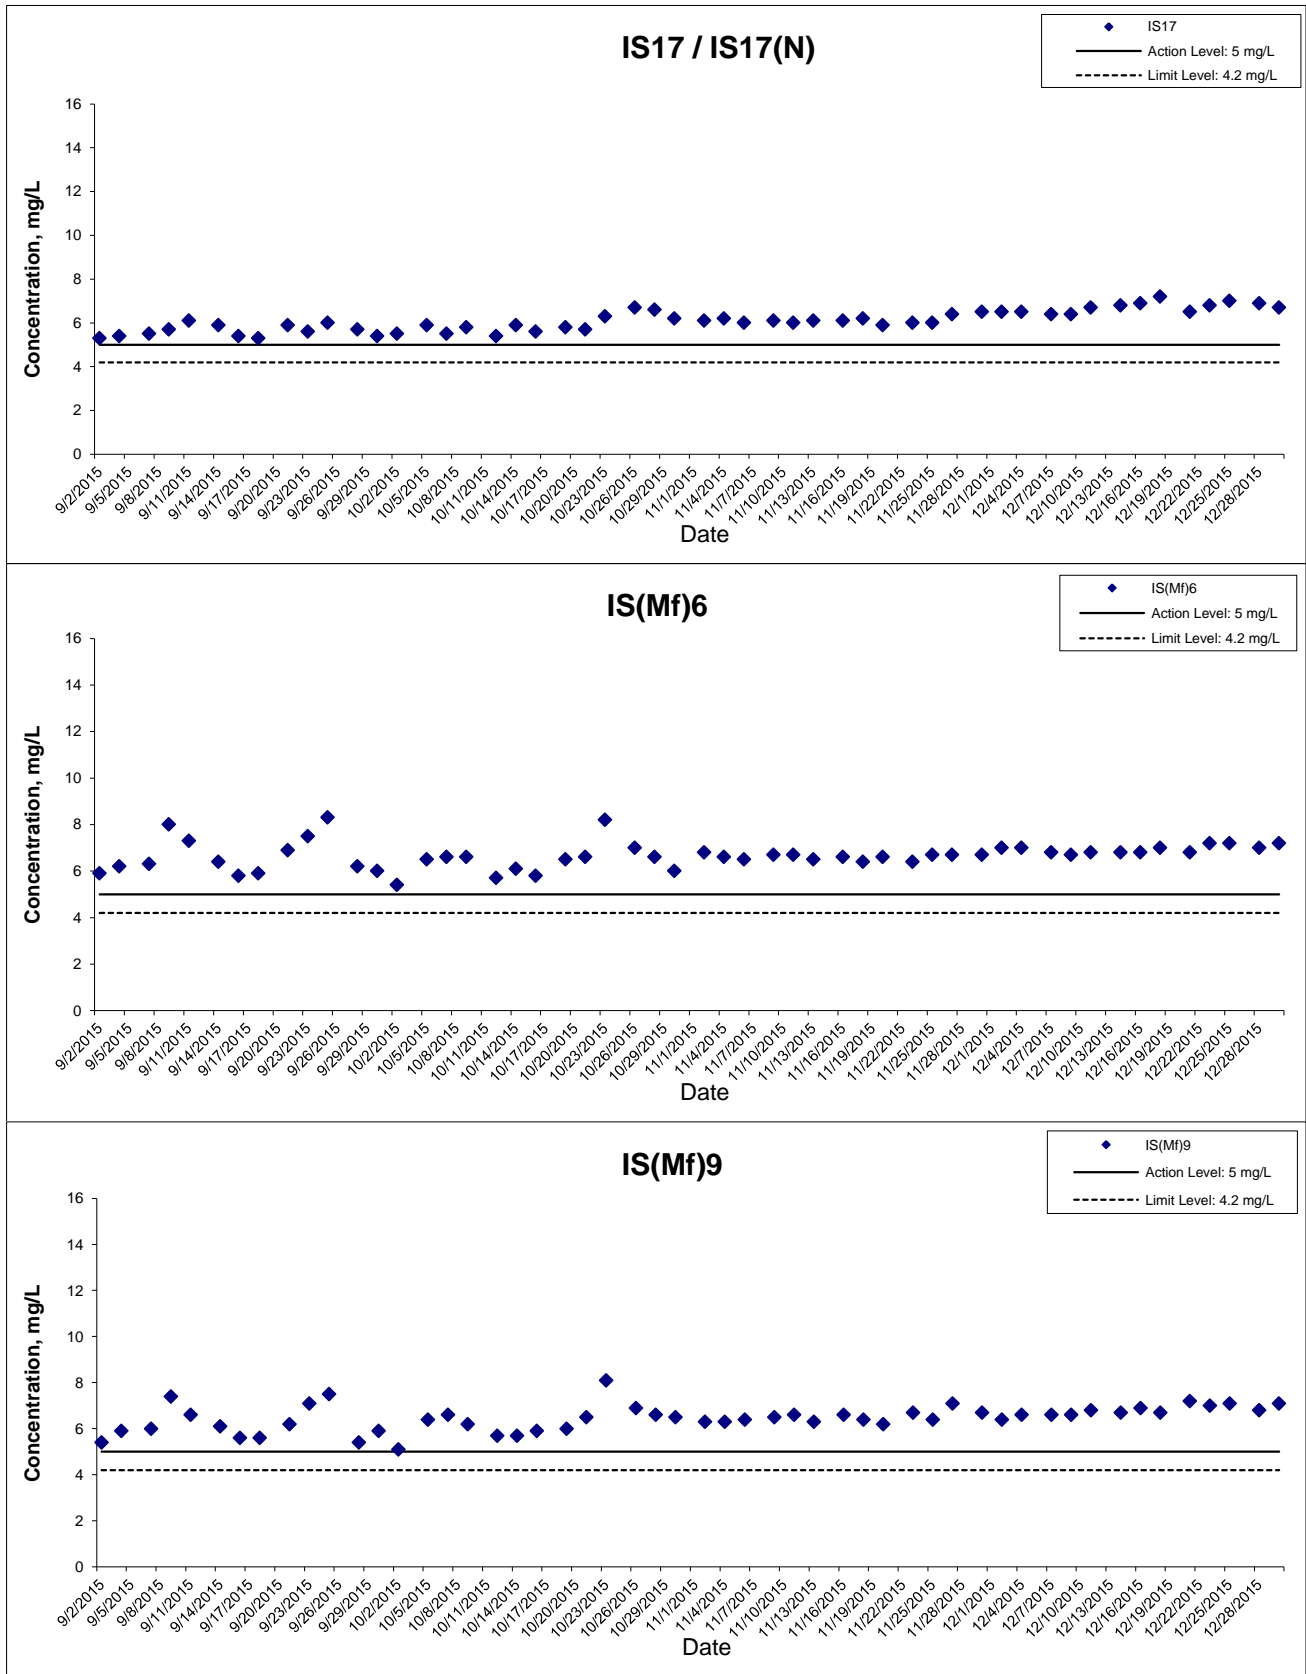

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.



Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

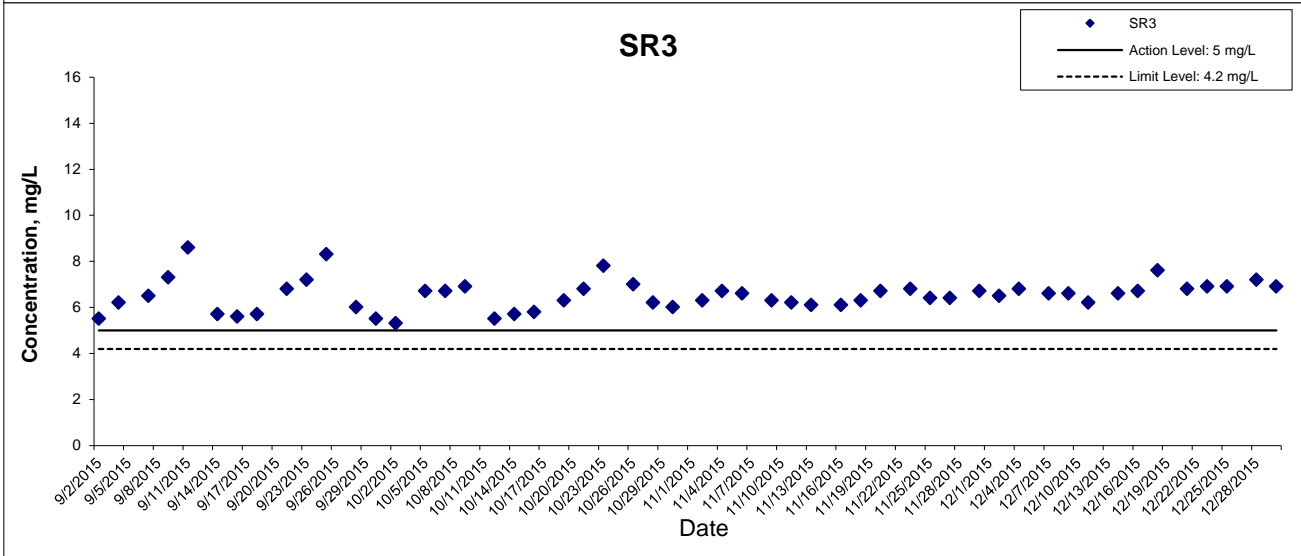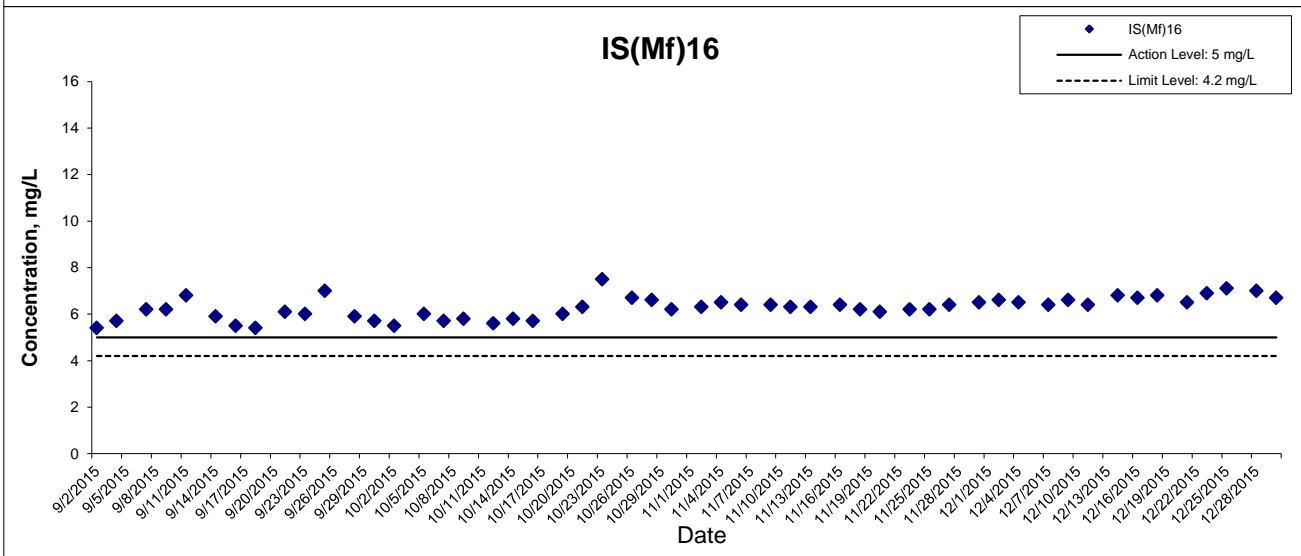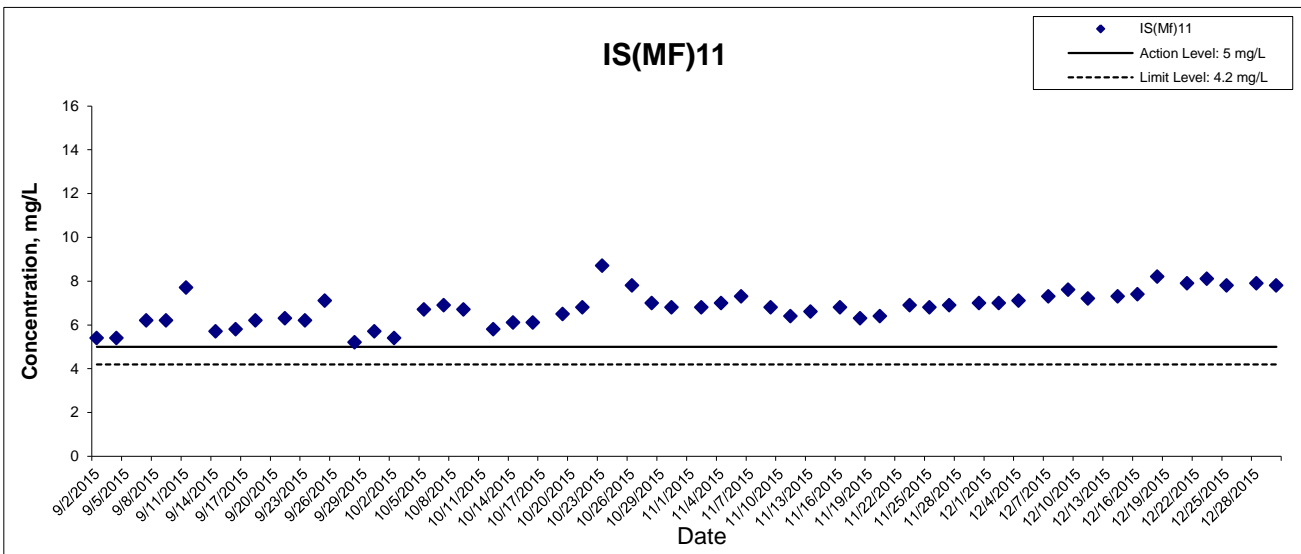


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results






Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

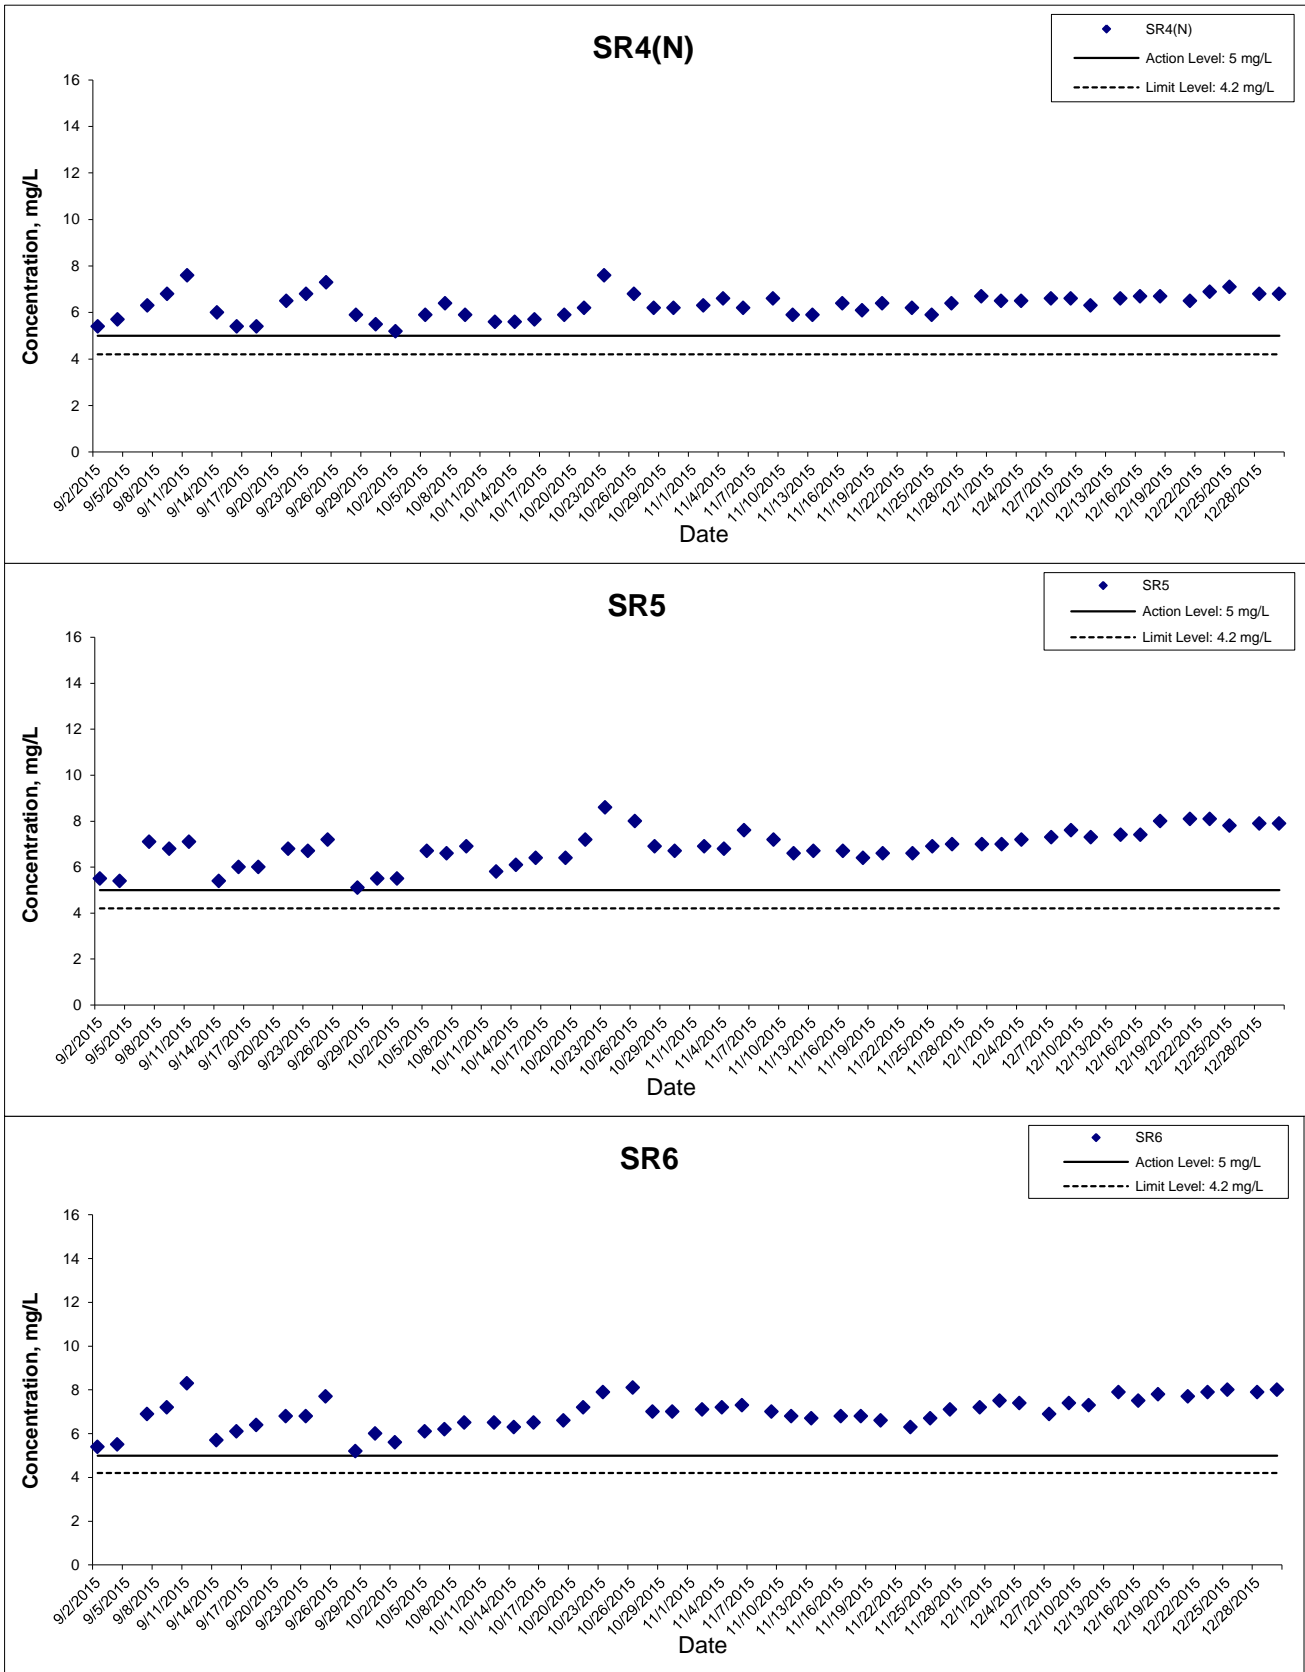

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

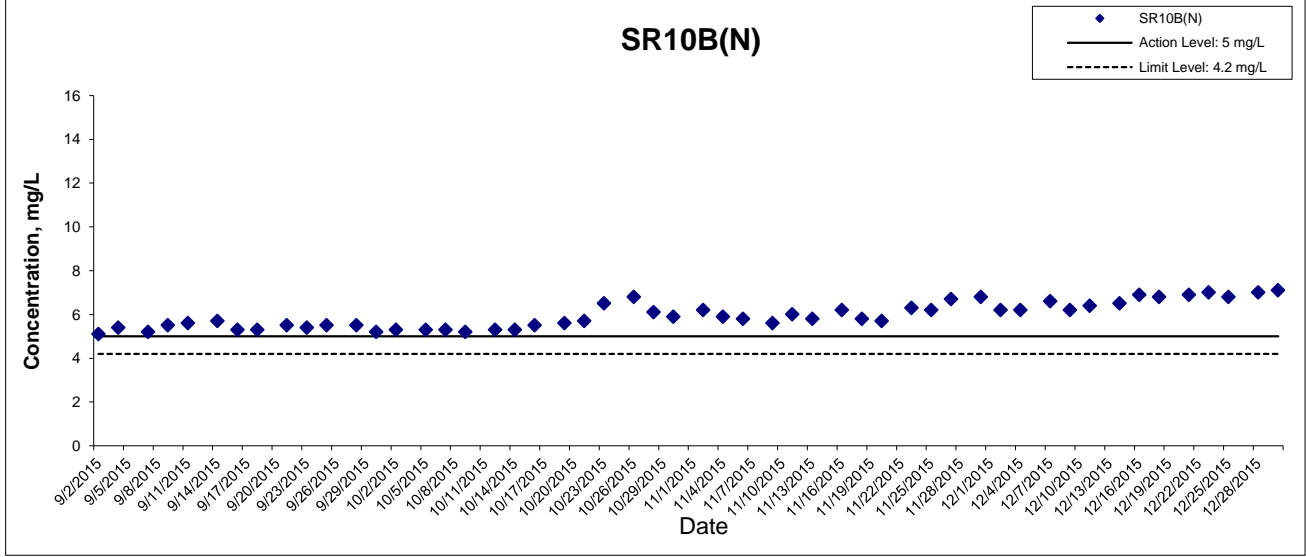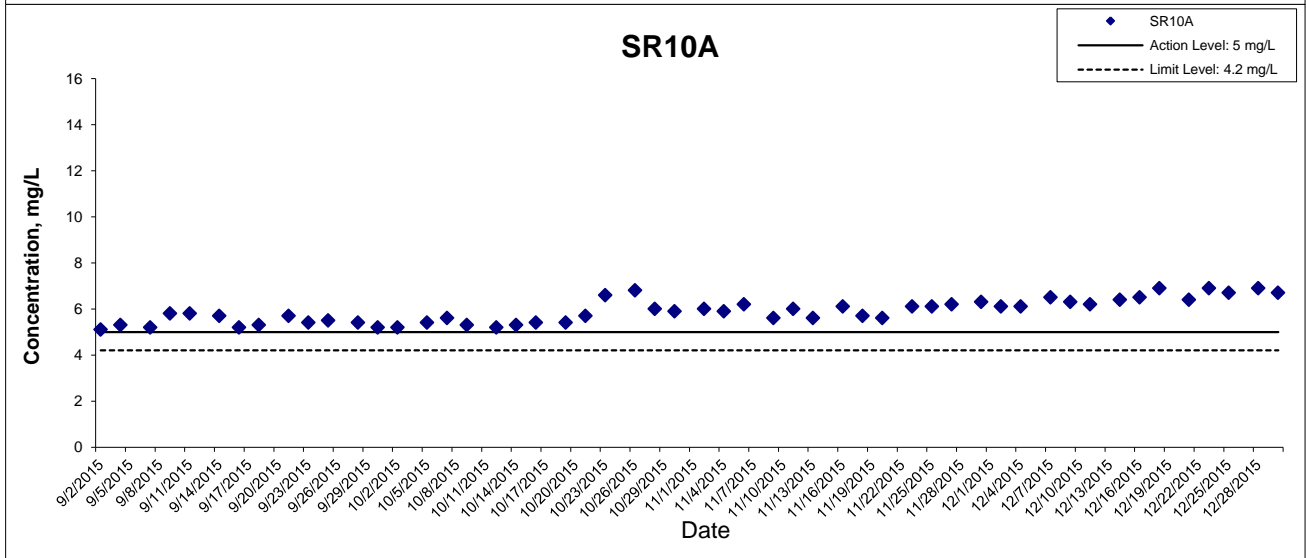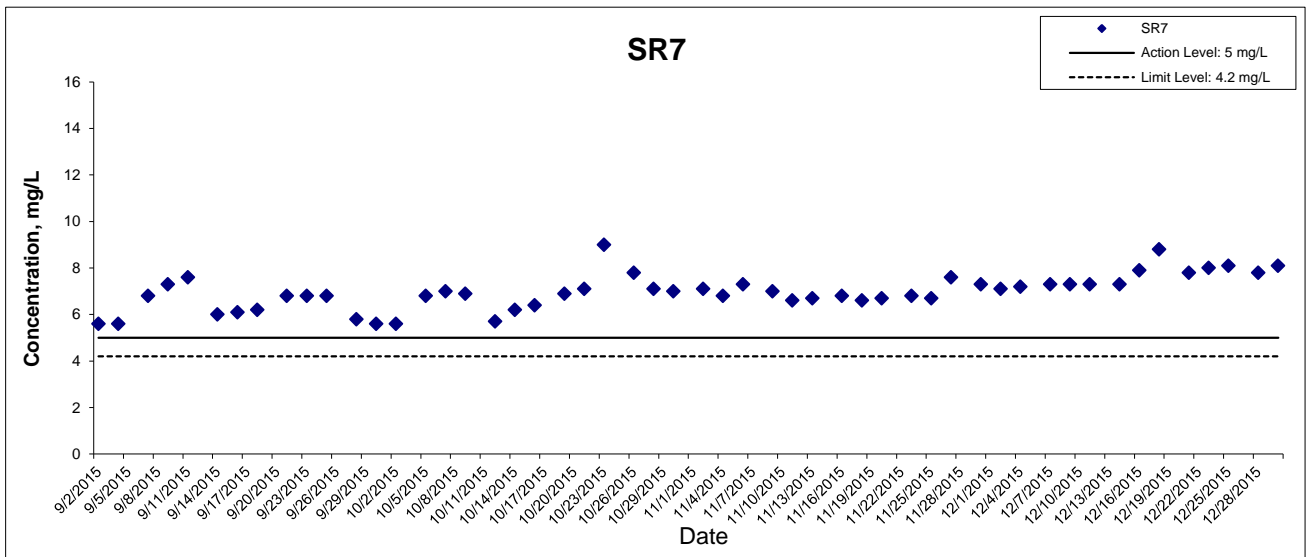


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

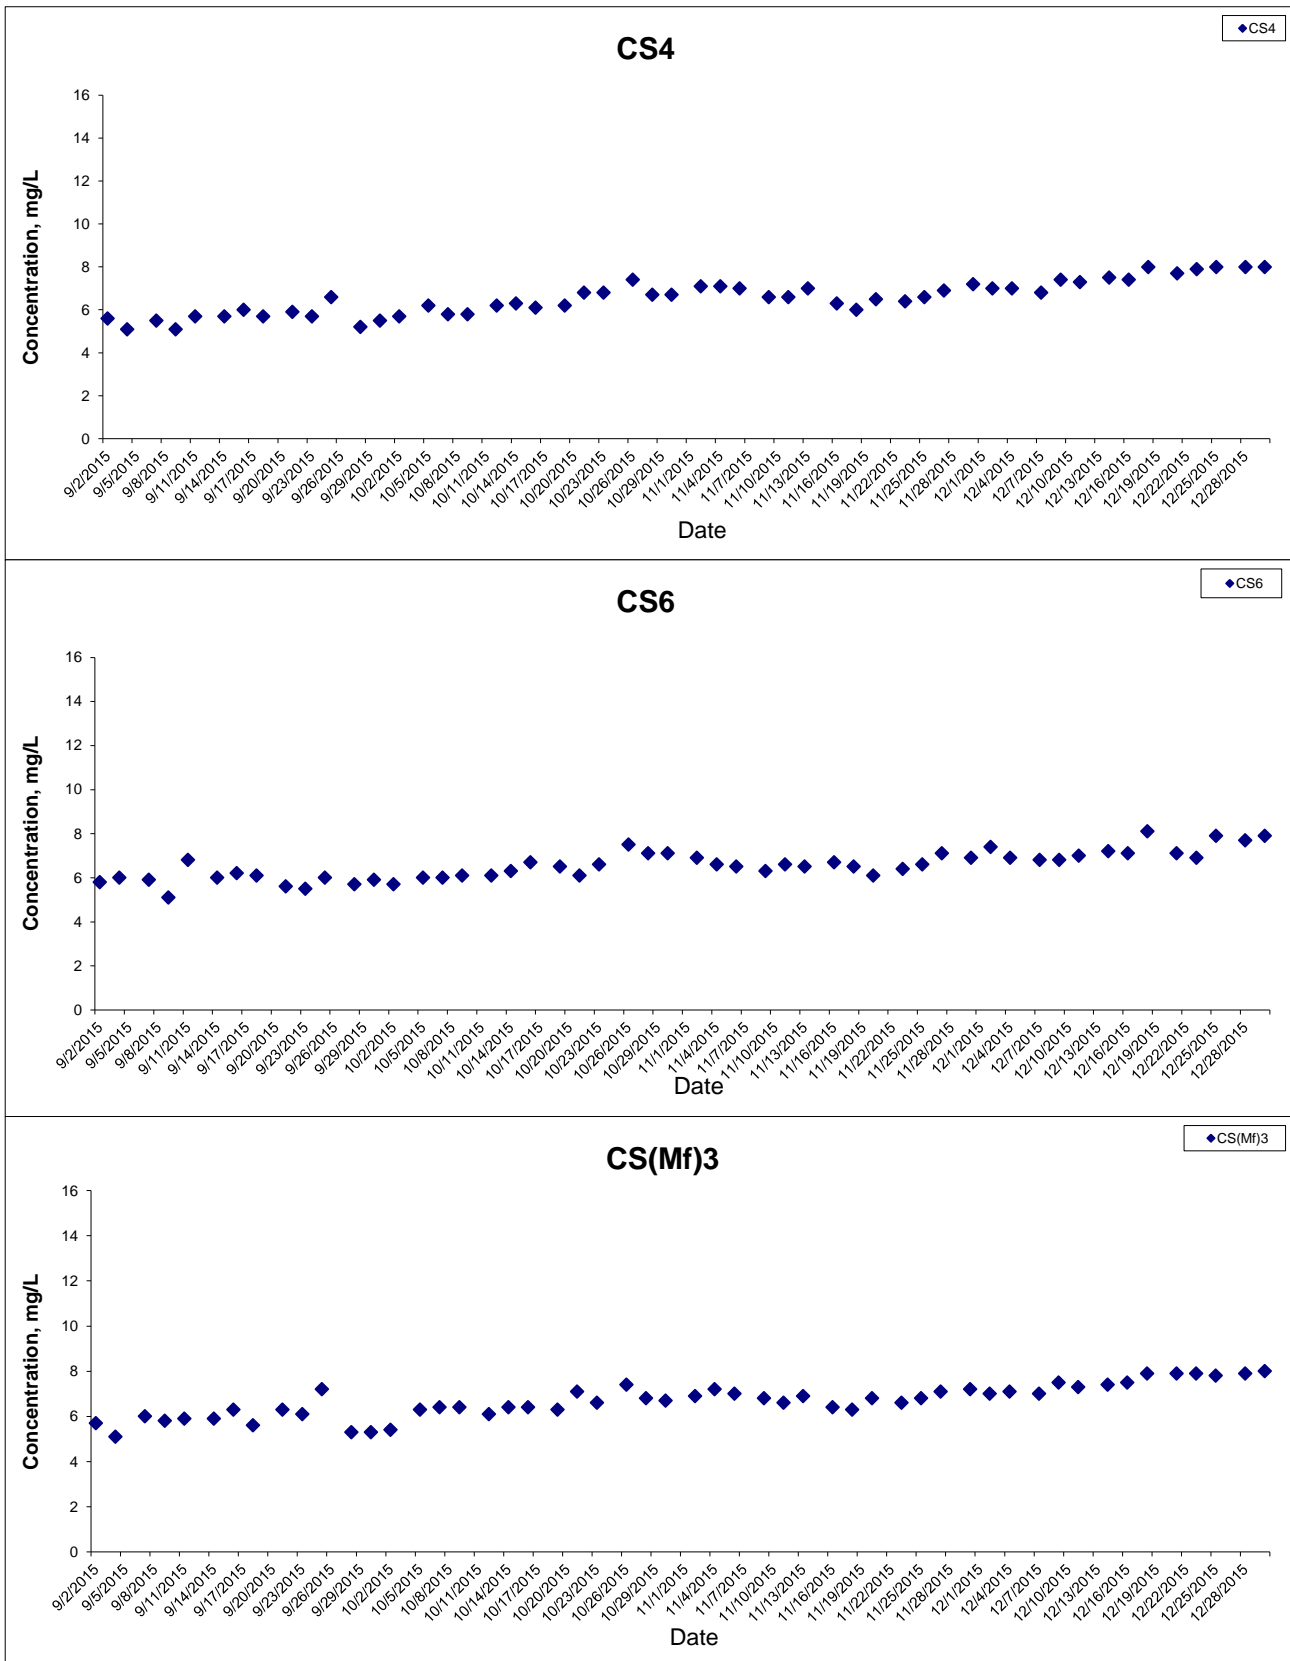




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results






Dissolved Oxygen (Bottom) at Mid-Ebb Tide

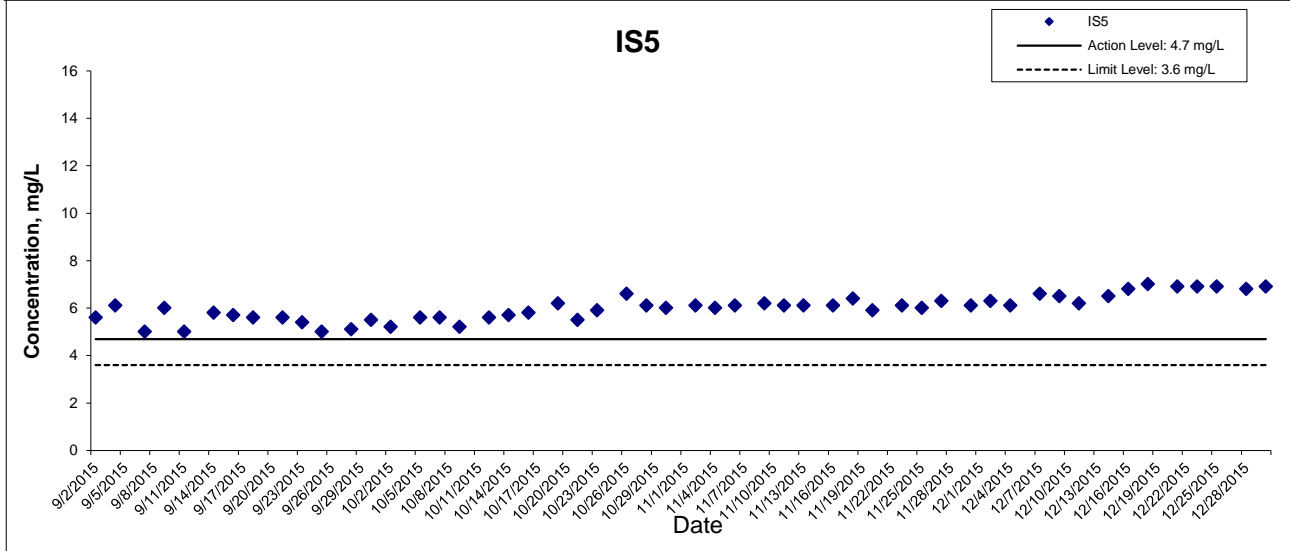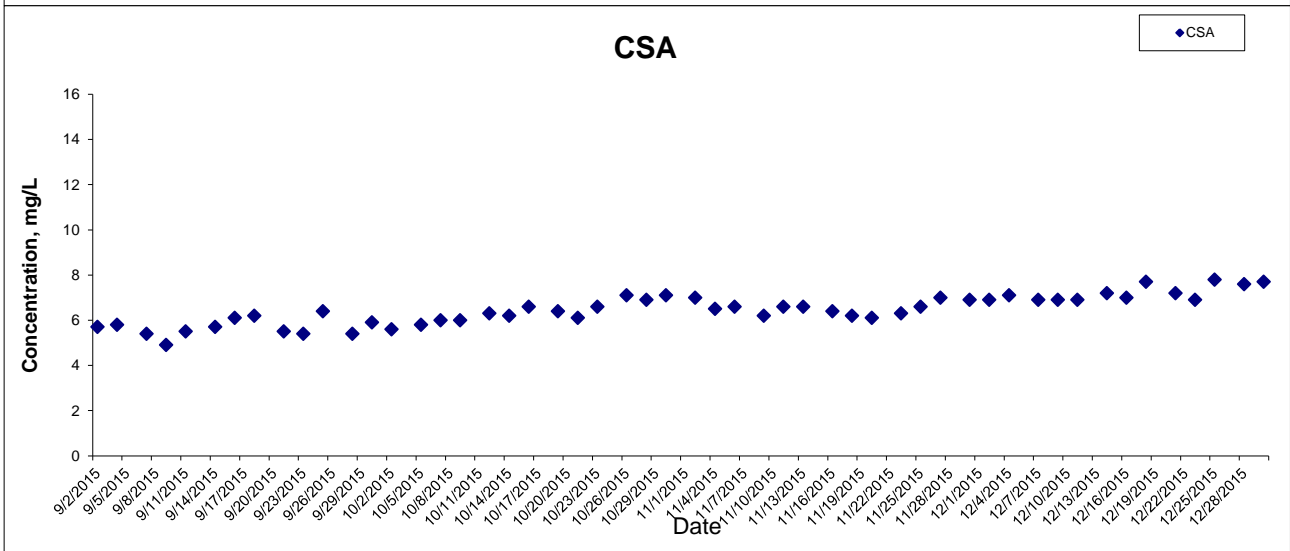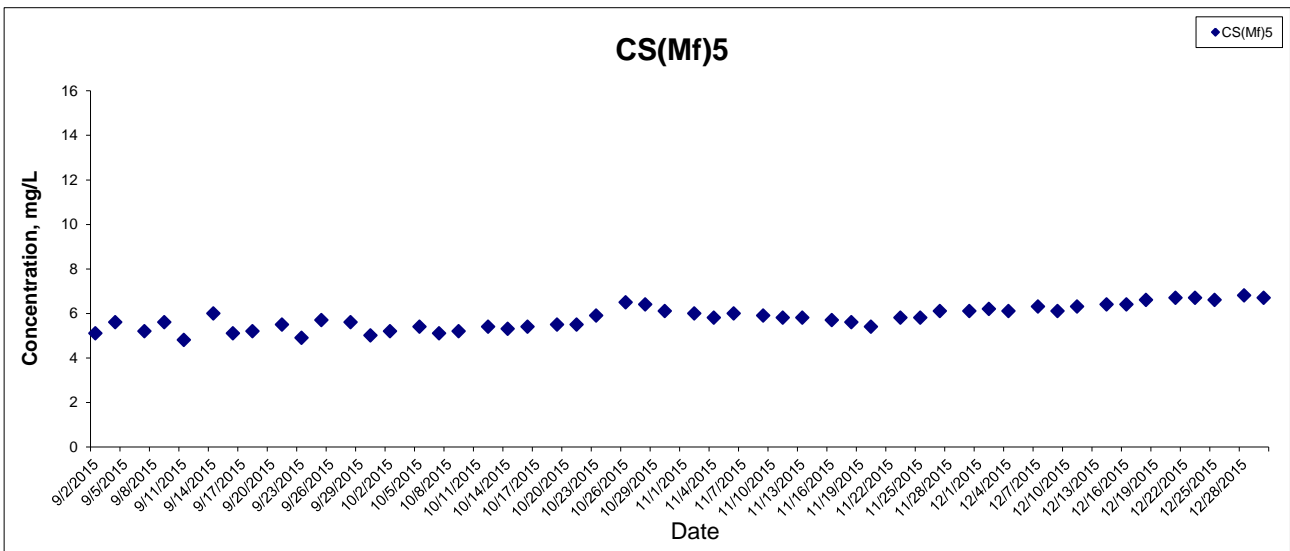

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

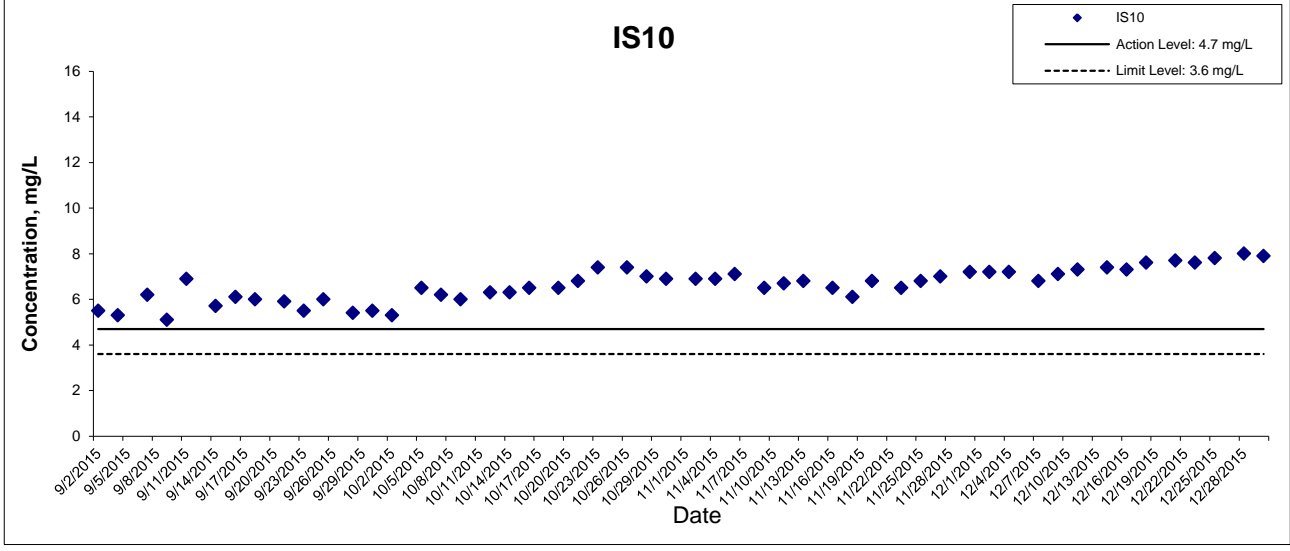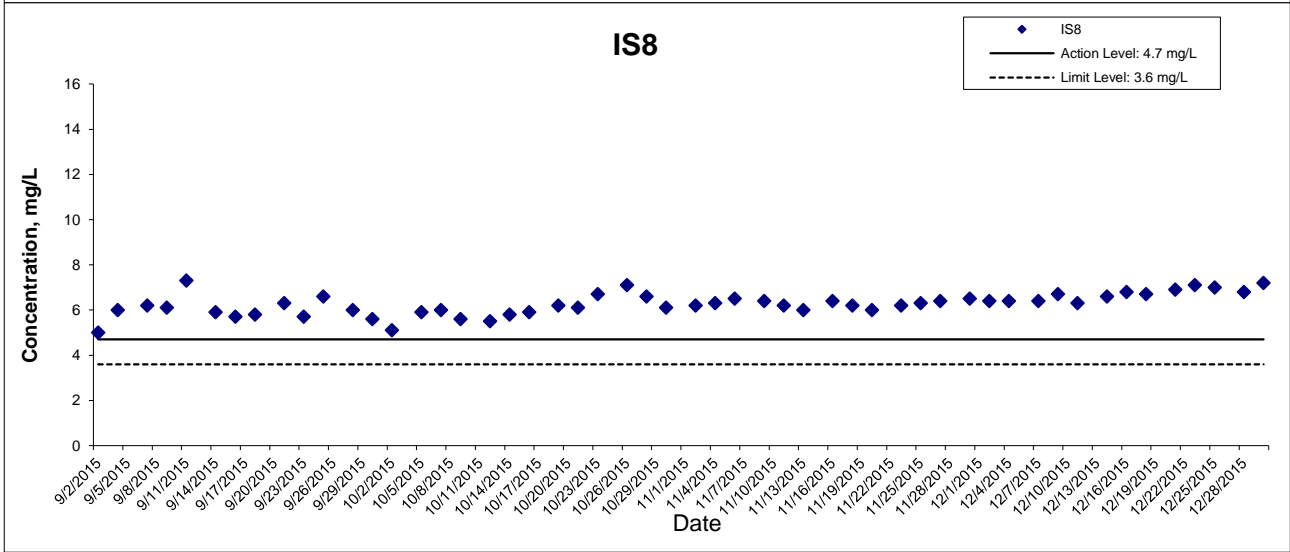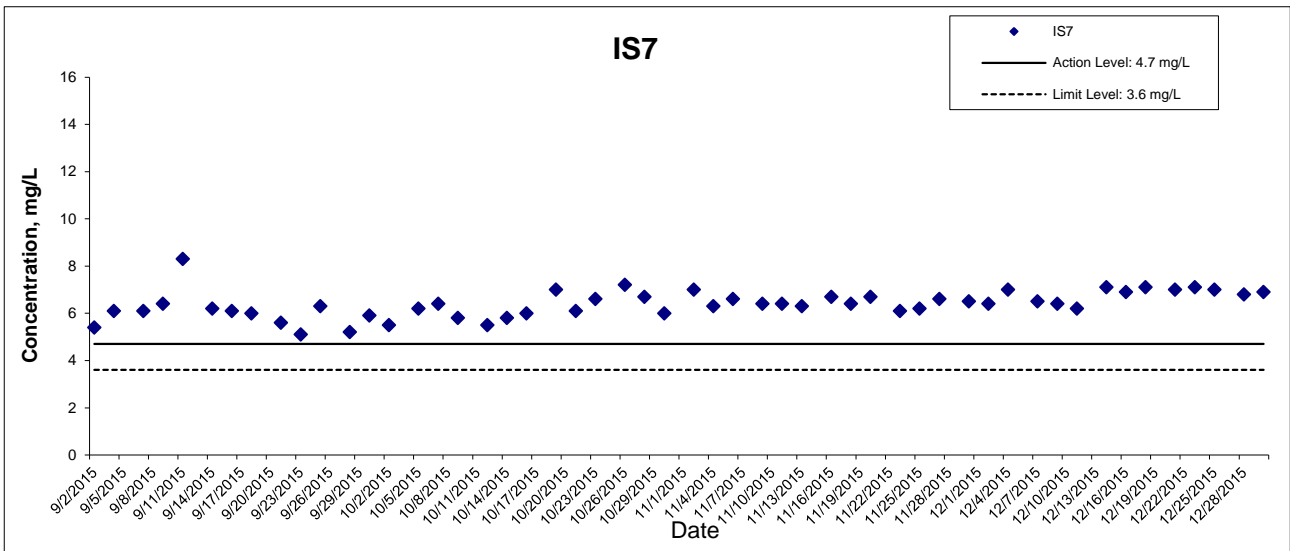




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

**HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS**

**Graphical Presentation of Impact Water Quality
Monitoring Results**






Dissolved Oxygen (Bottom) at Mid-Ebb Tide

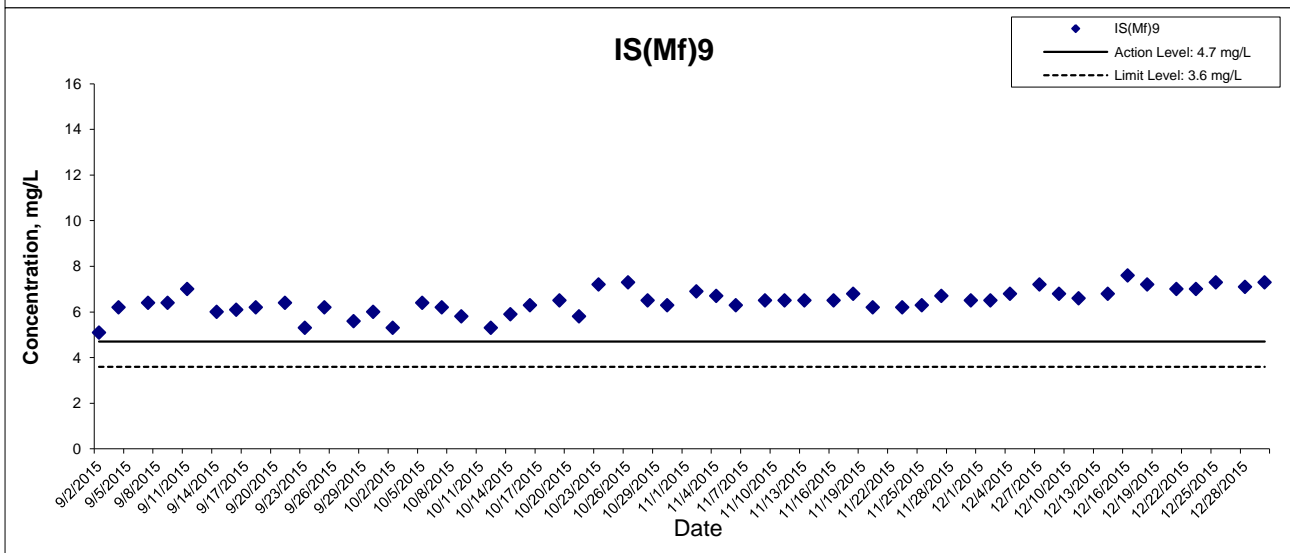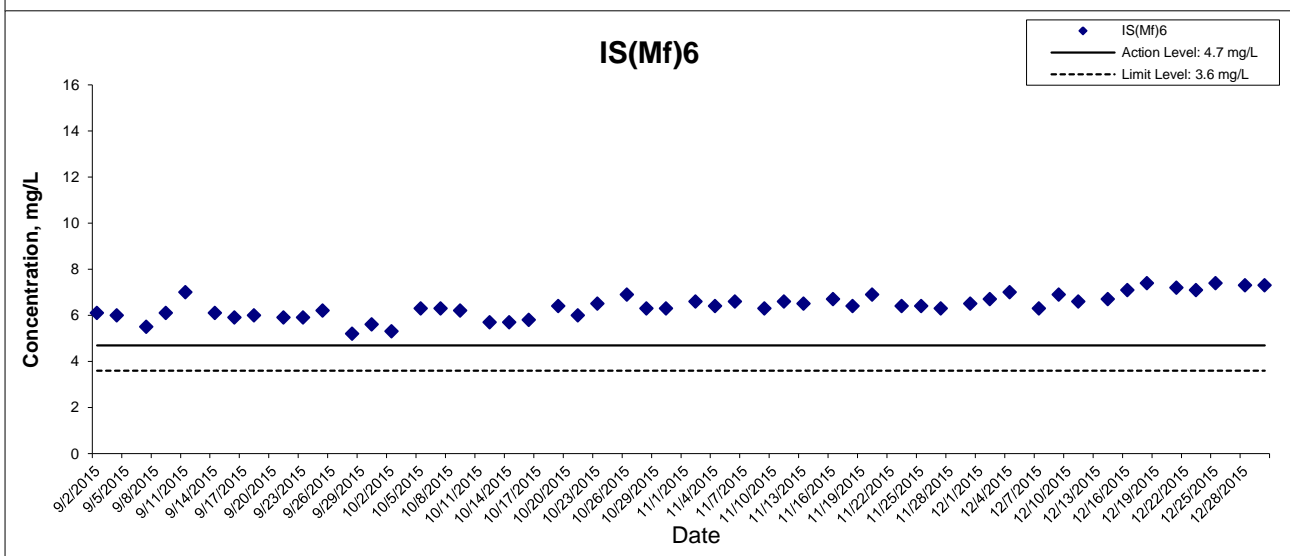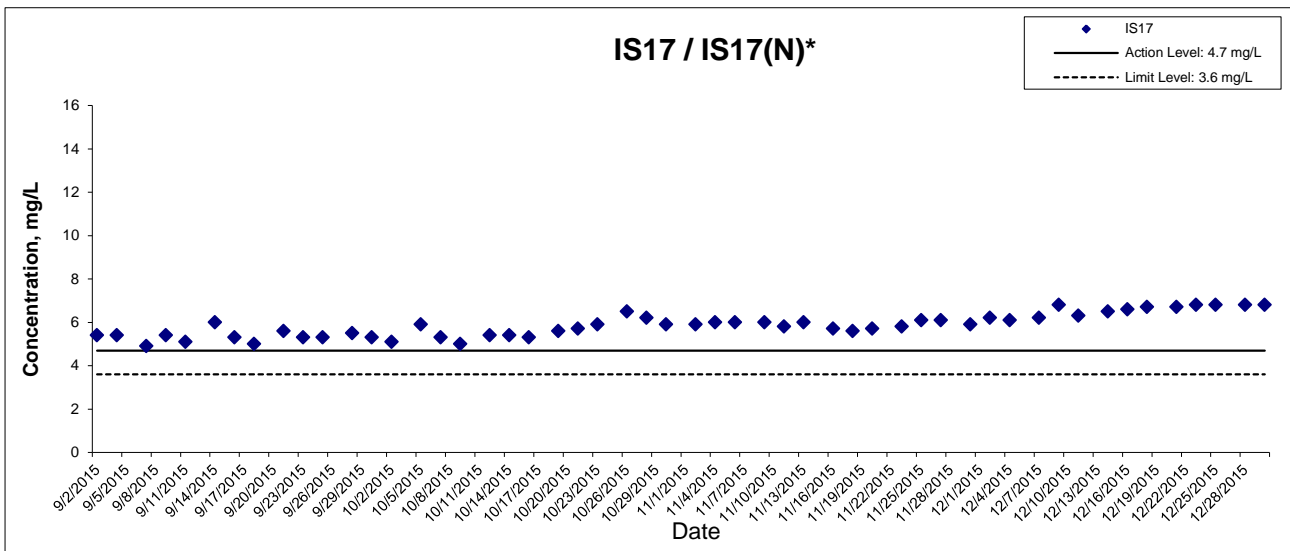

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Dissolved Oxygen (Bottom) at Mid-Ebb Tide

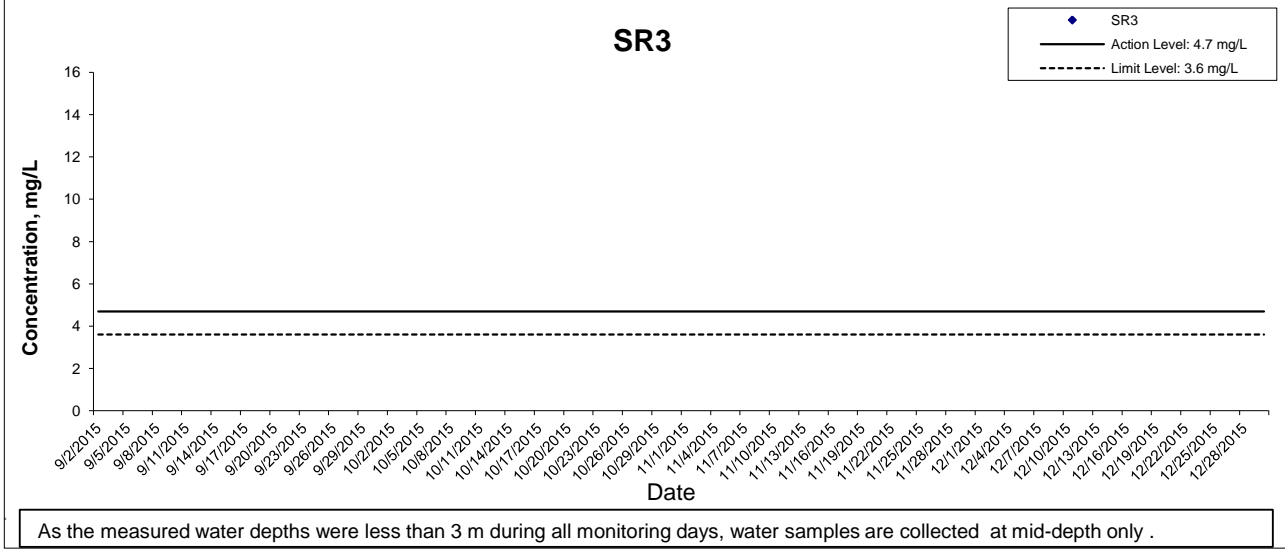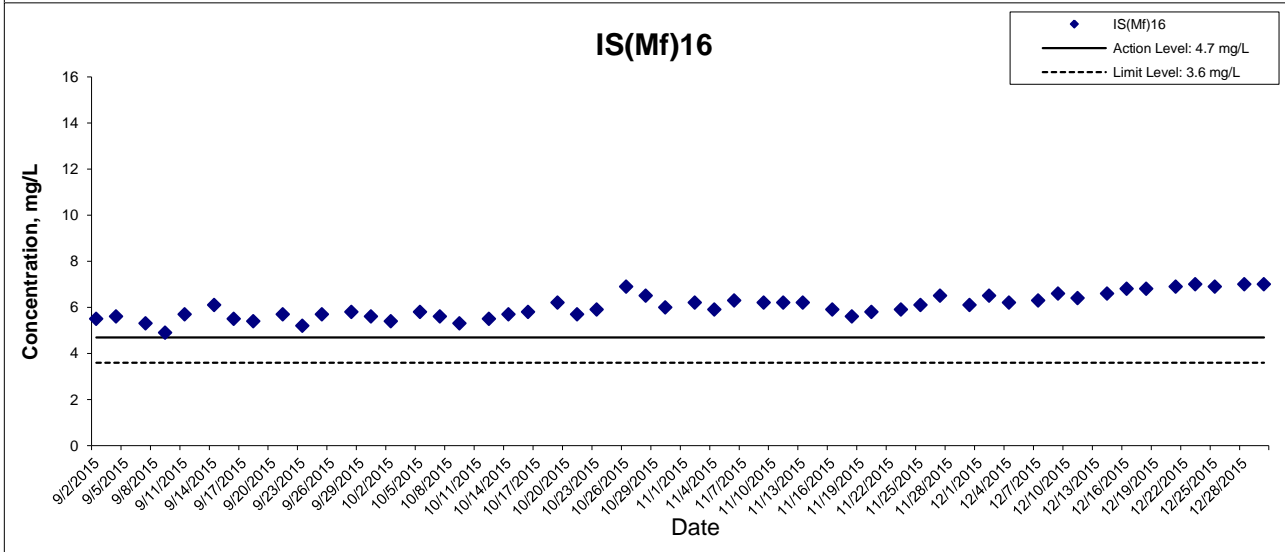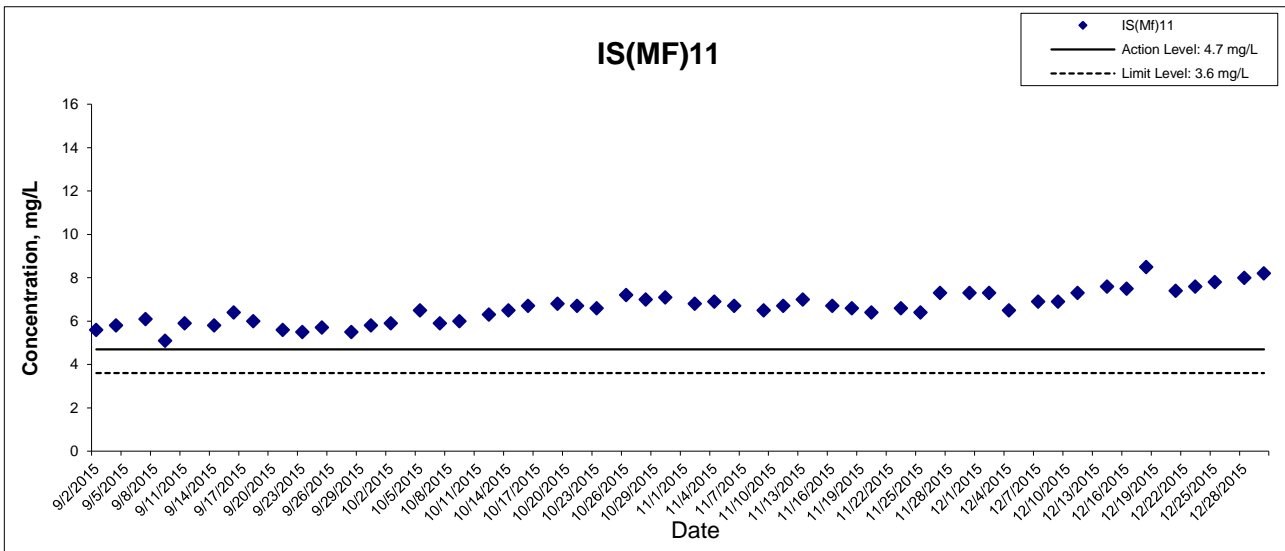

As the measured water depths were less than 3 m during all monitoring days, water samples are collected at mid-depth only .




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

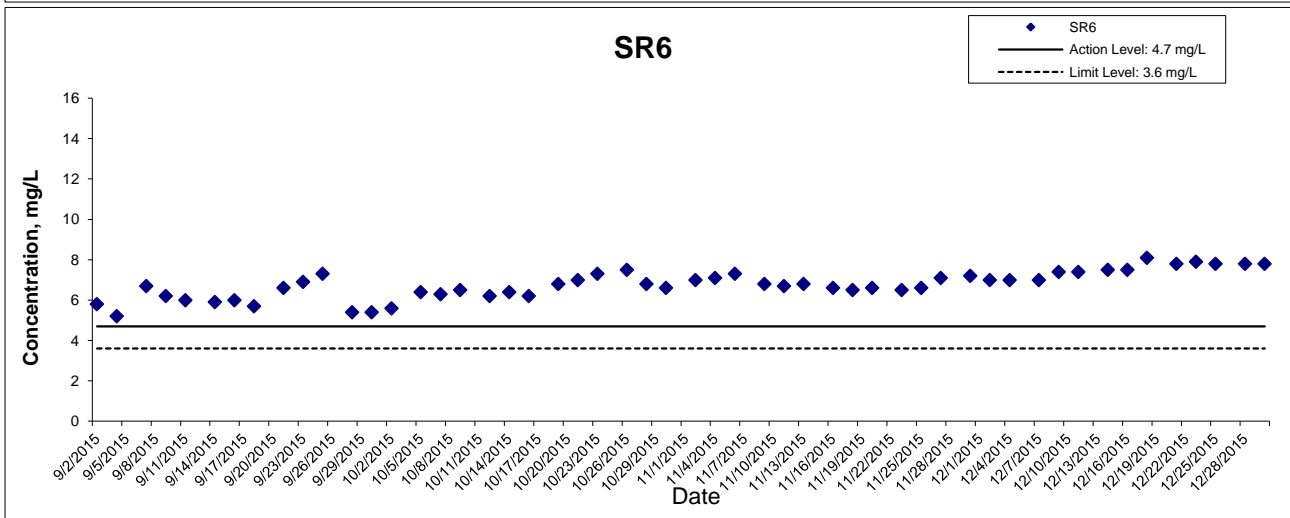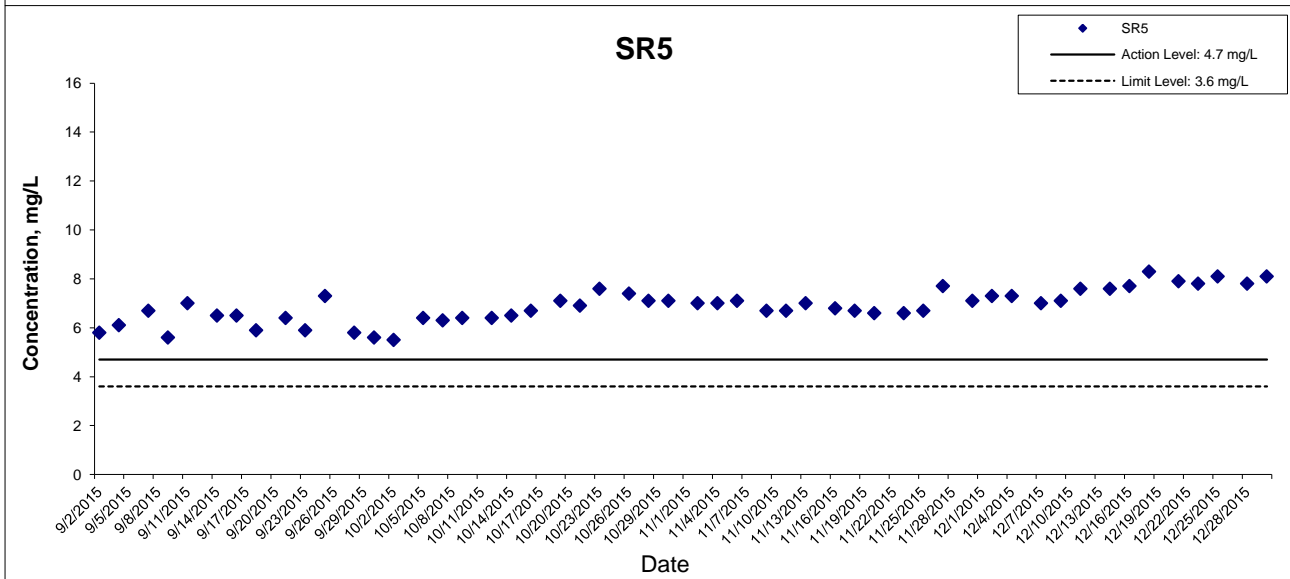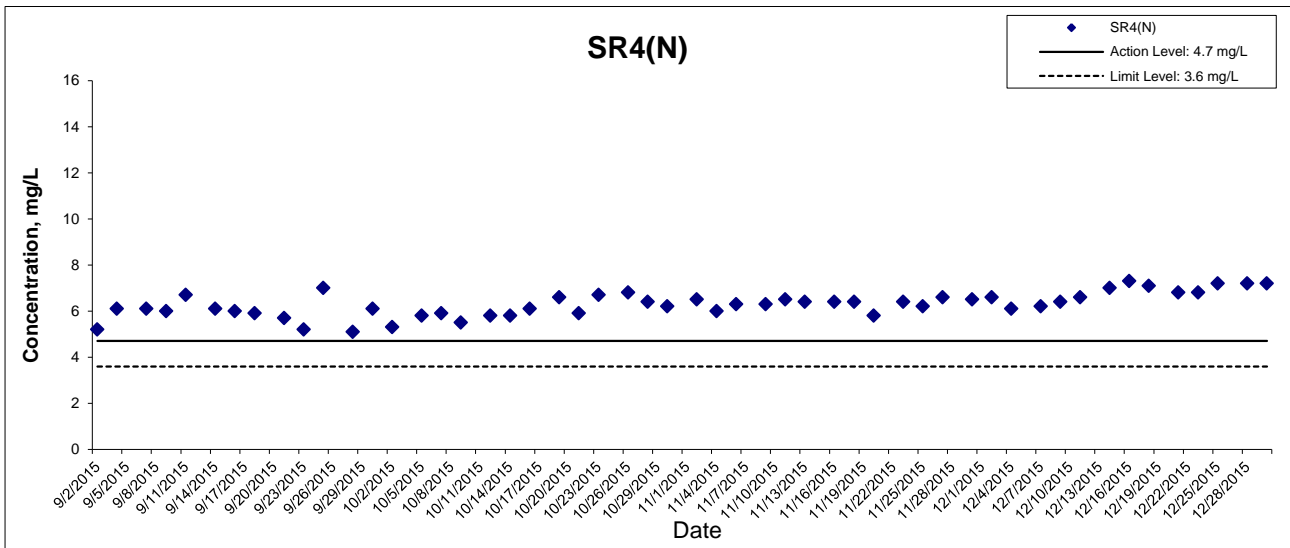


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

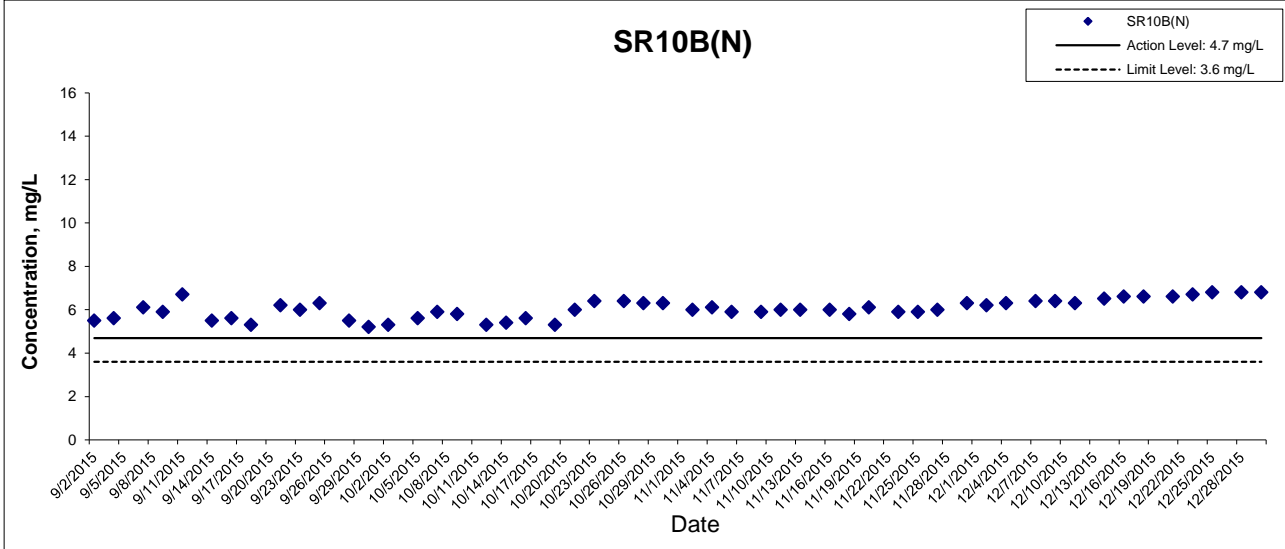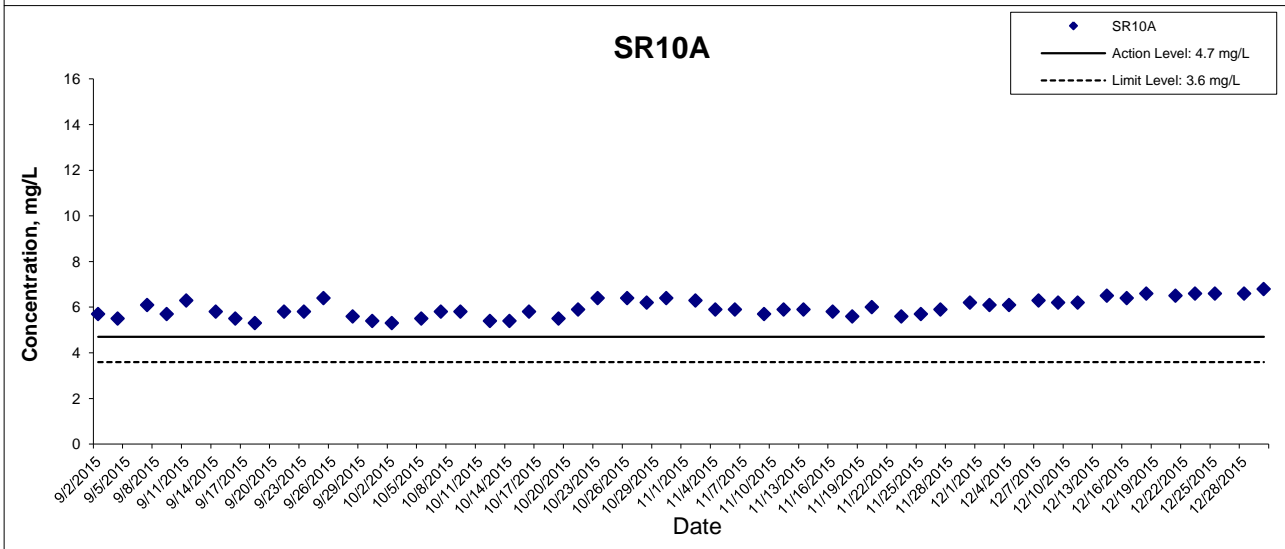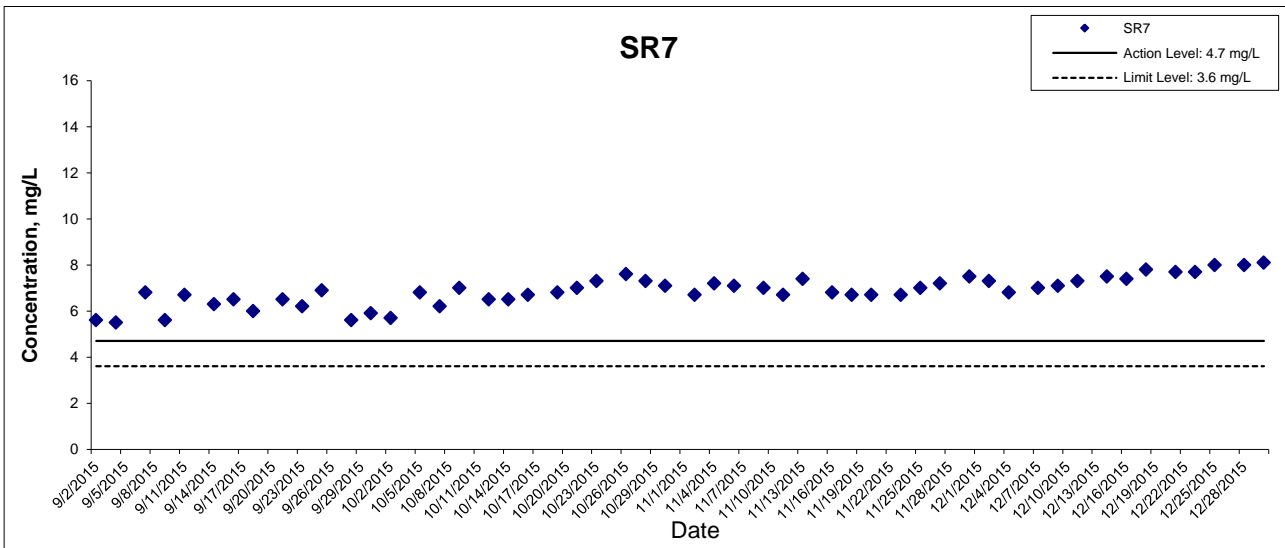

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

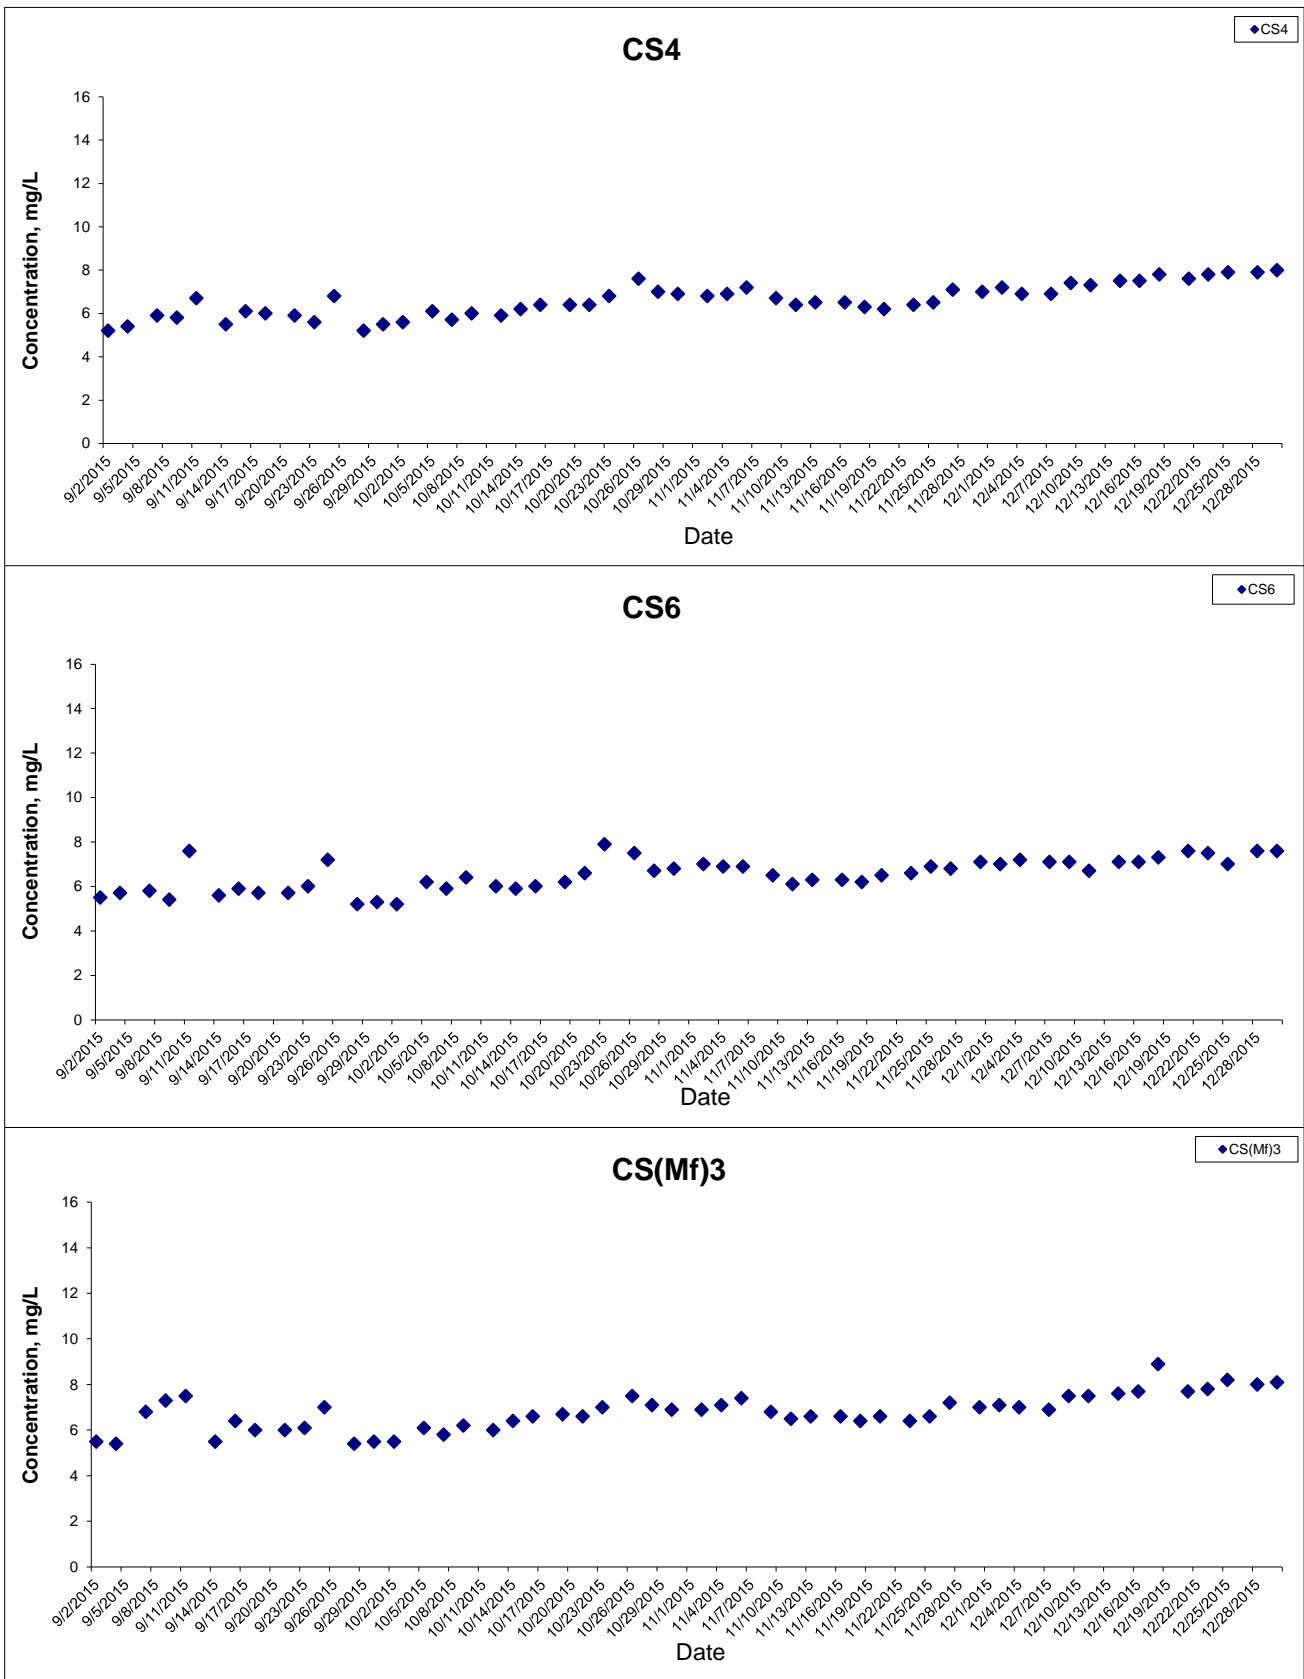


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results






Dissolved Oxygen (Bottom) at Mid-Flood Tide

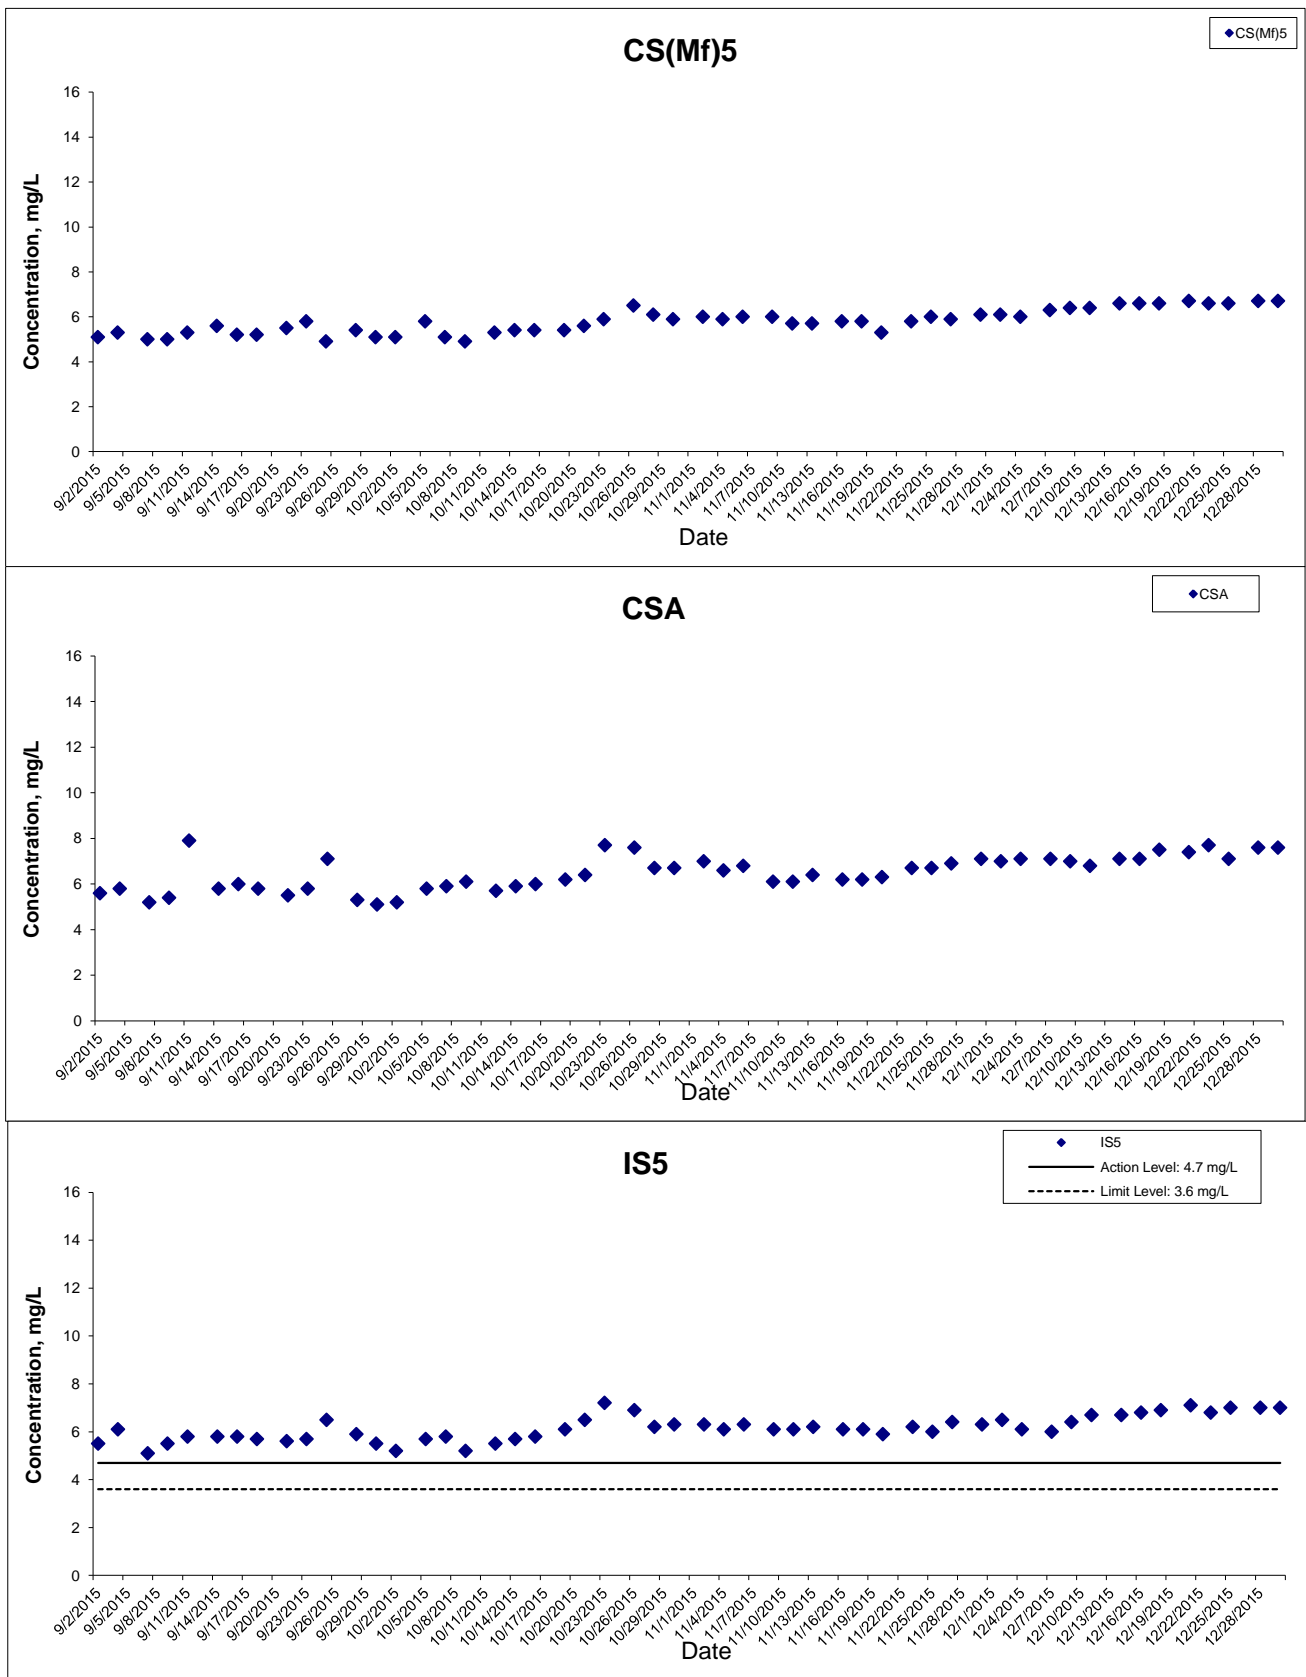

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.



Dissolved Oxygen (Bottom) at Mid-Flood Tide

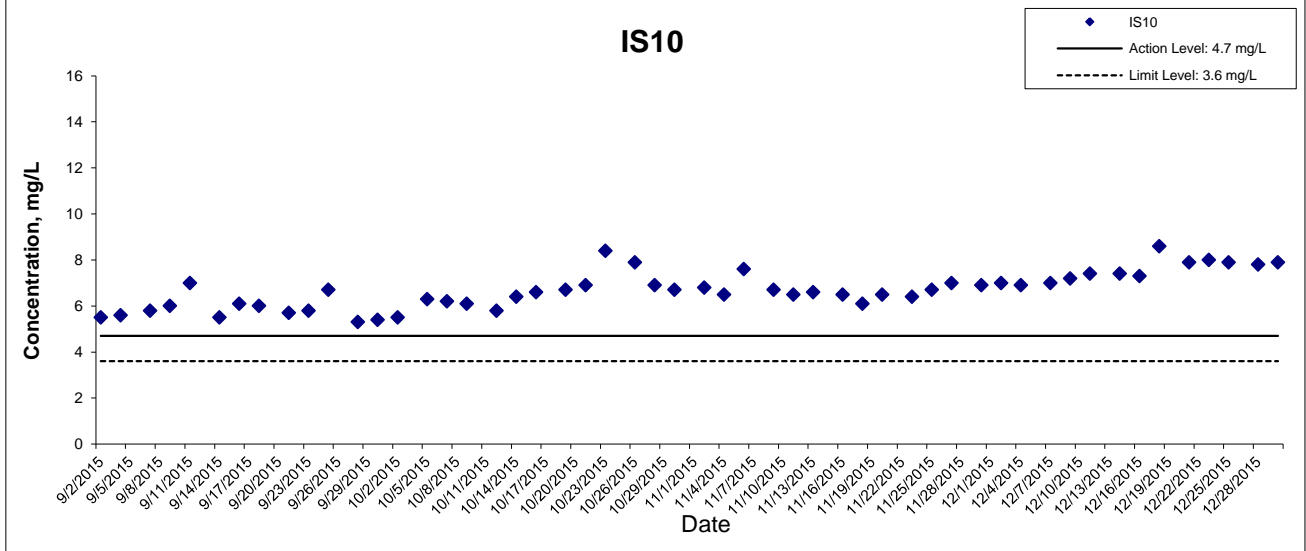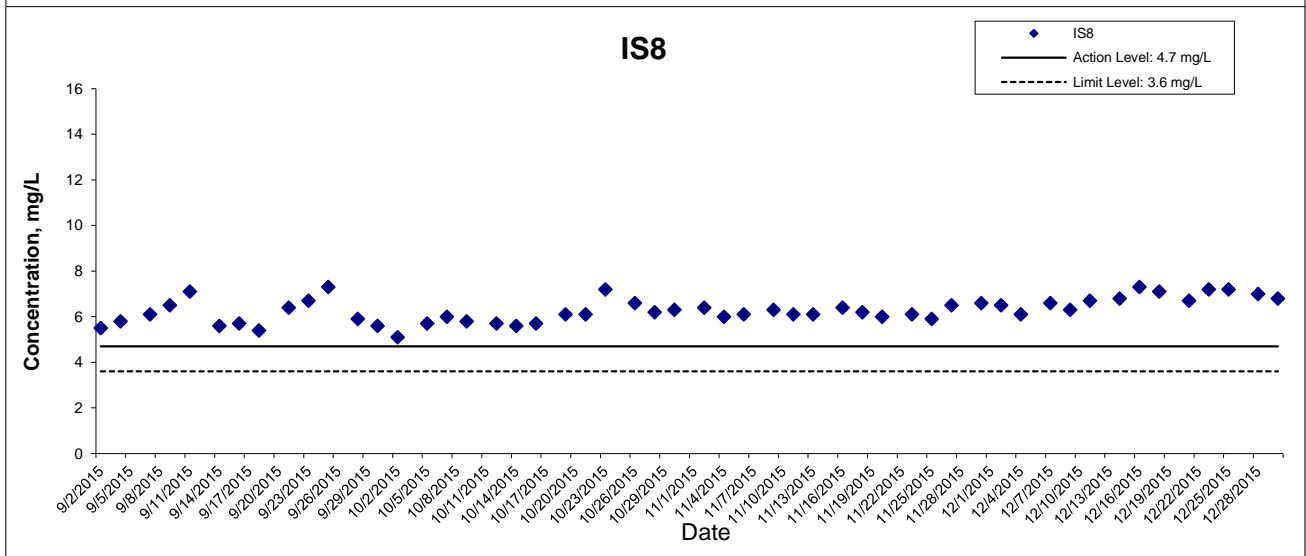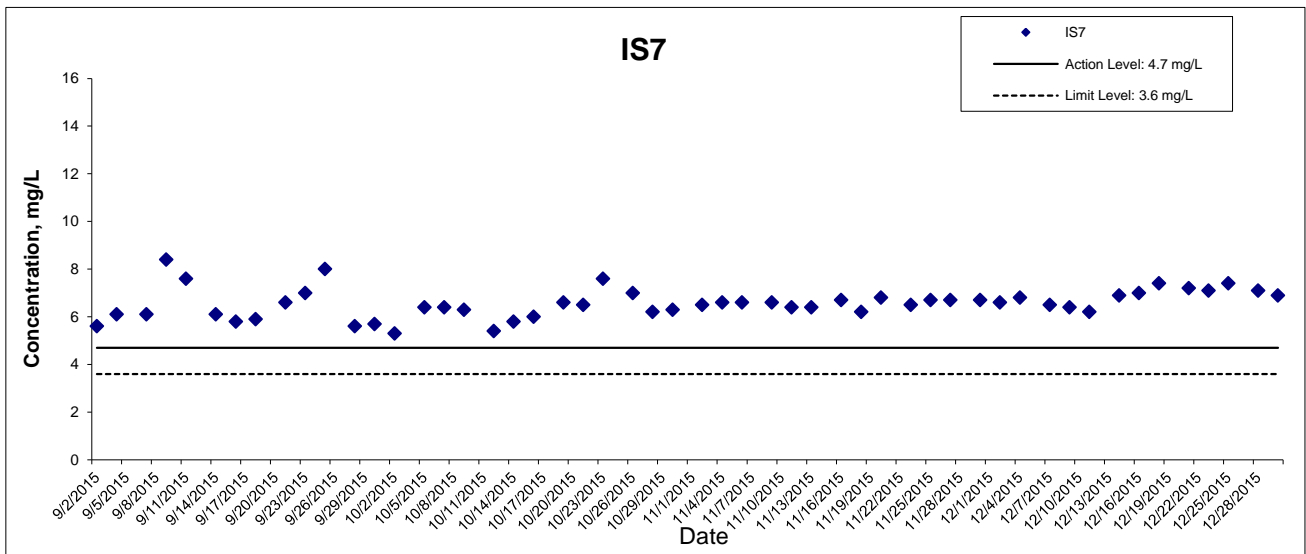

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

**HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS**

**Graphical Presentation of Impact Water Quality
 Monitoring Results**




Project No.: 60249820

Date: January 2016




Appendix J

Dissolved Oxygen (Bottom) at Mid-Flood Tide

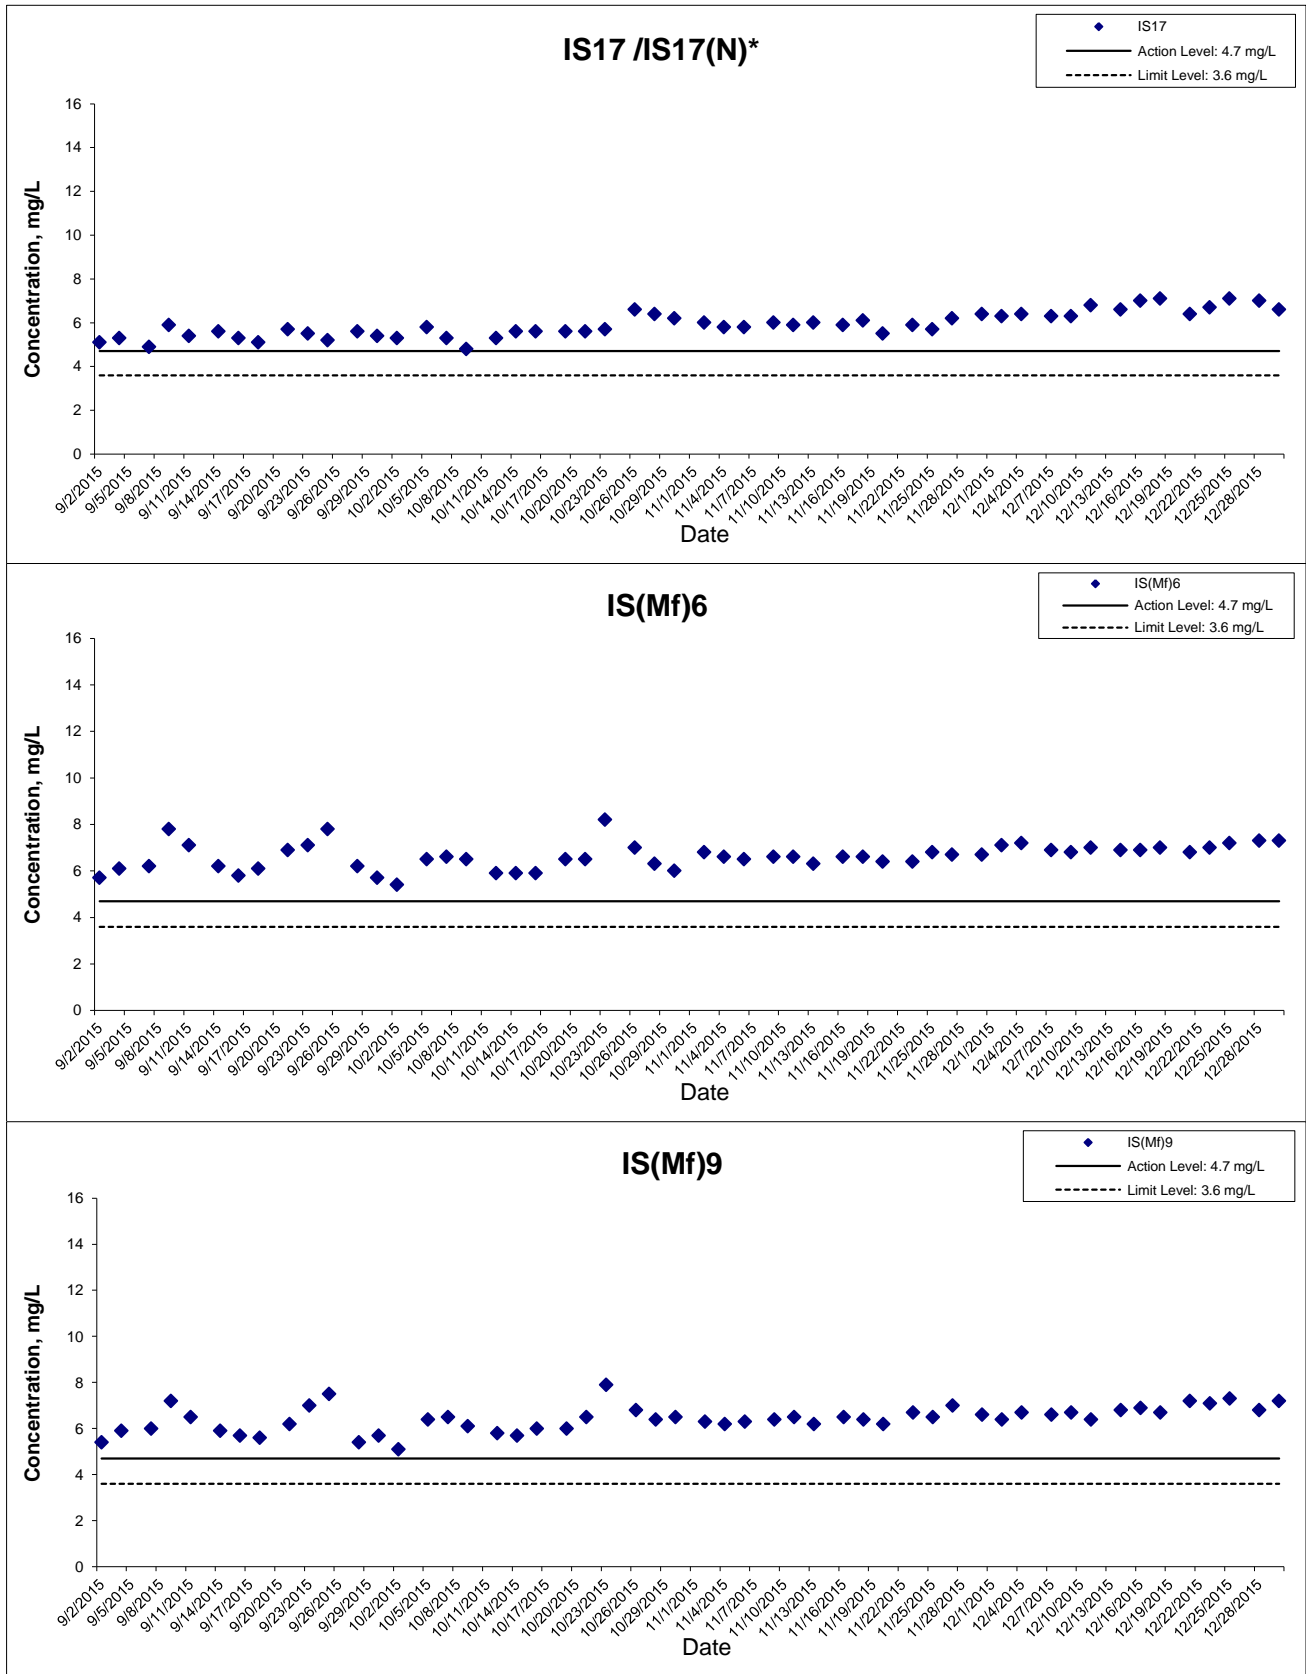

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Dissolved Oxygen (Bottom) at Mid-Flood Tide

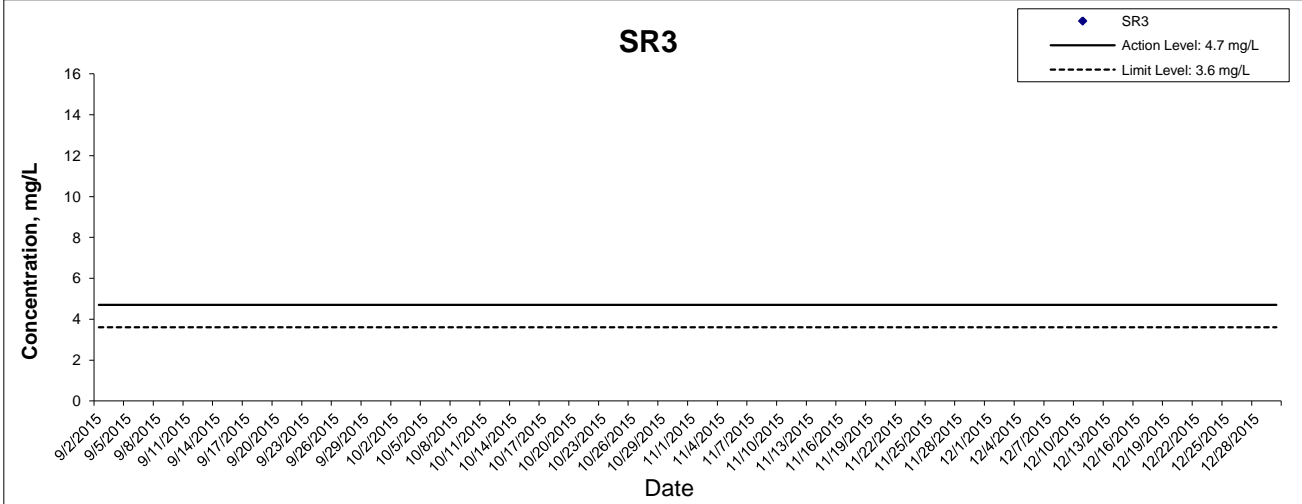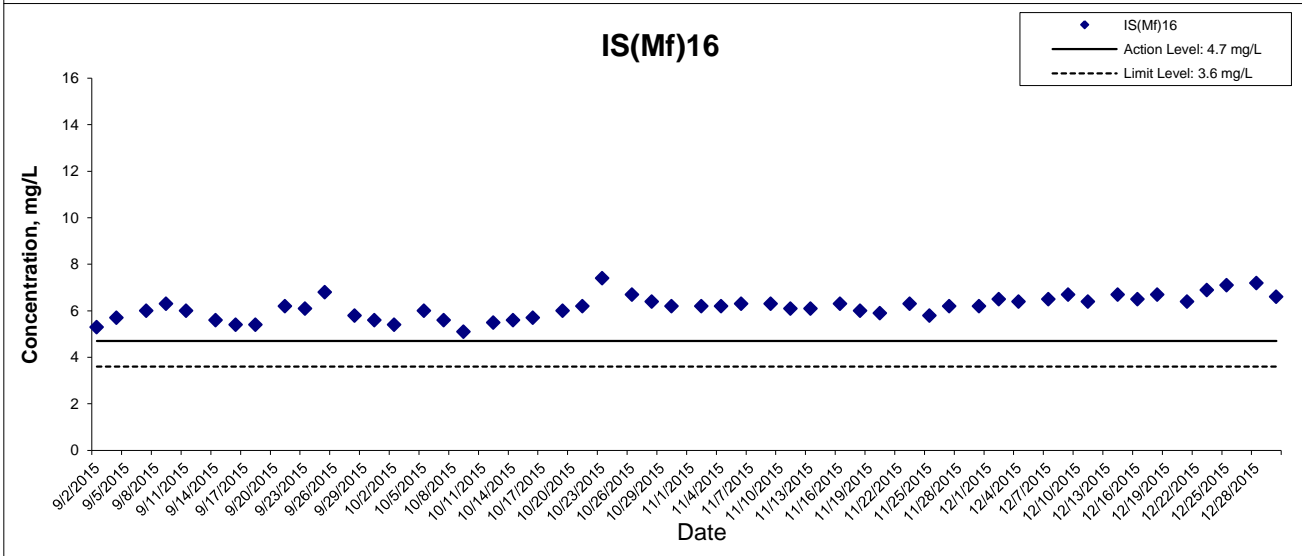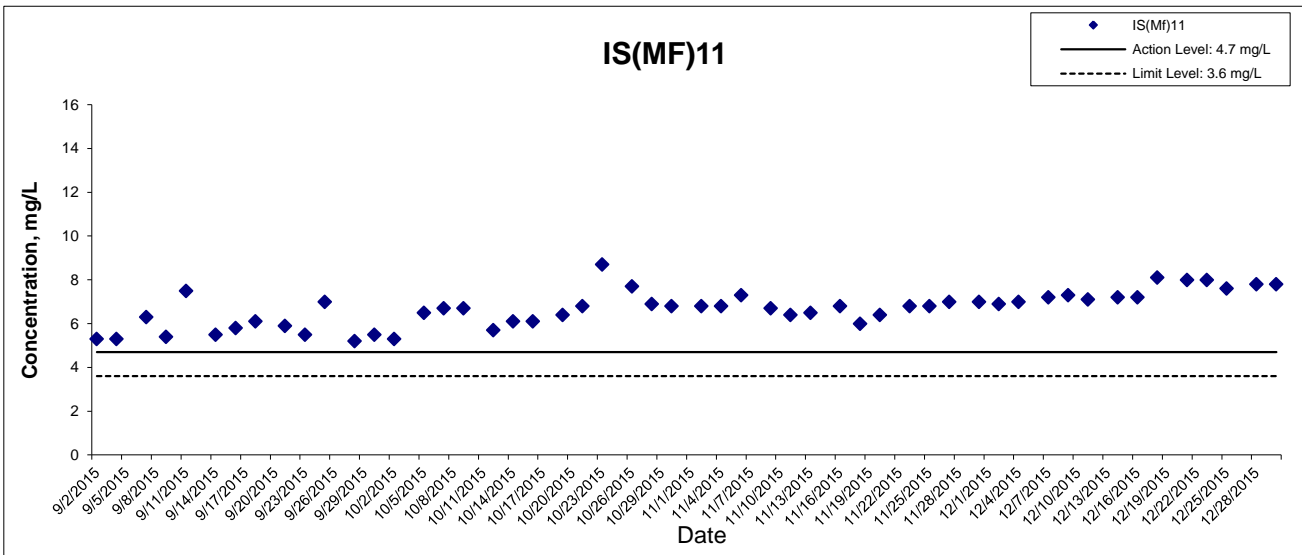

As the measured water depths were less than 3 m during all monitoring days, water samples are collected at mid-depth only .




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

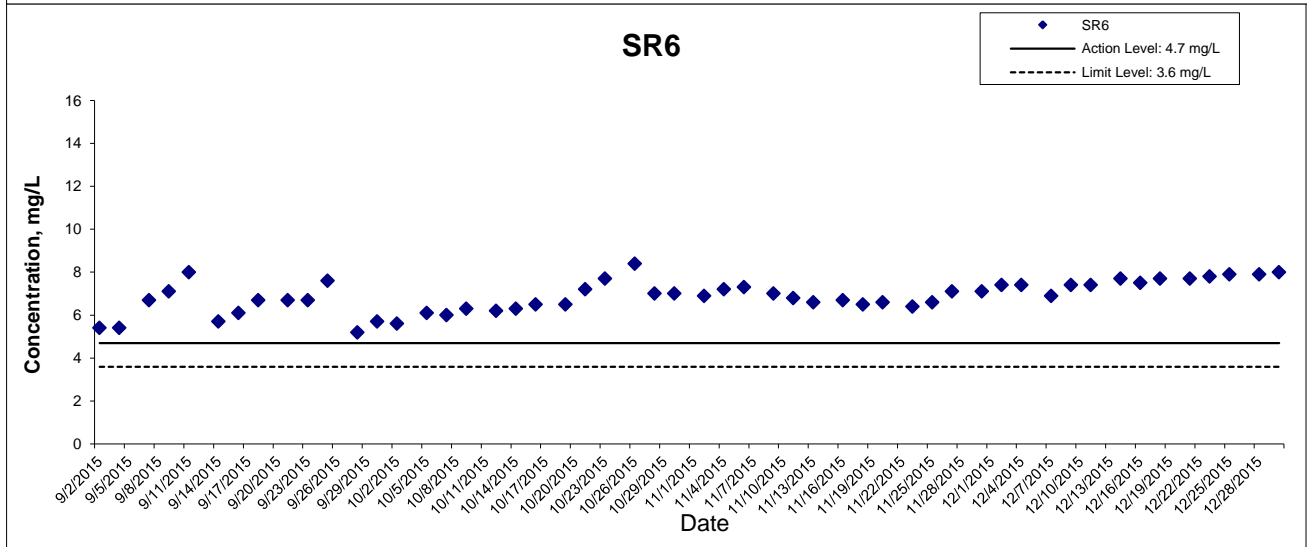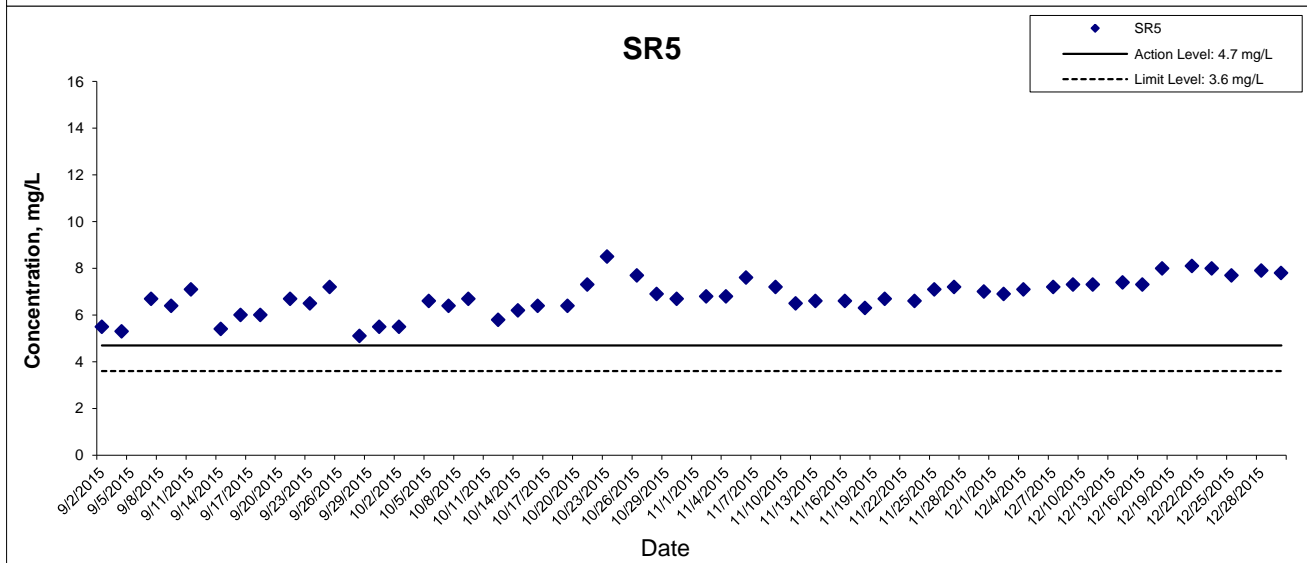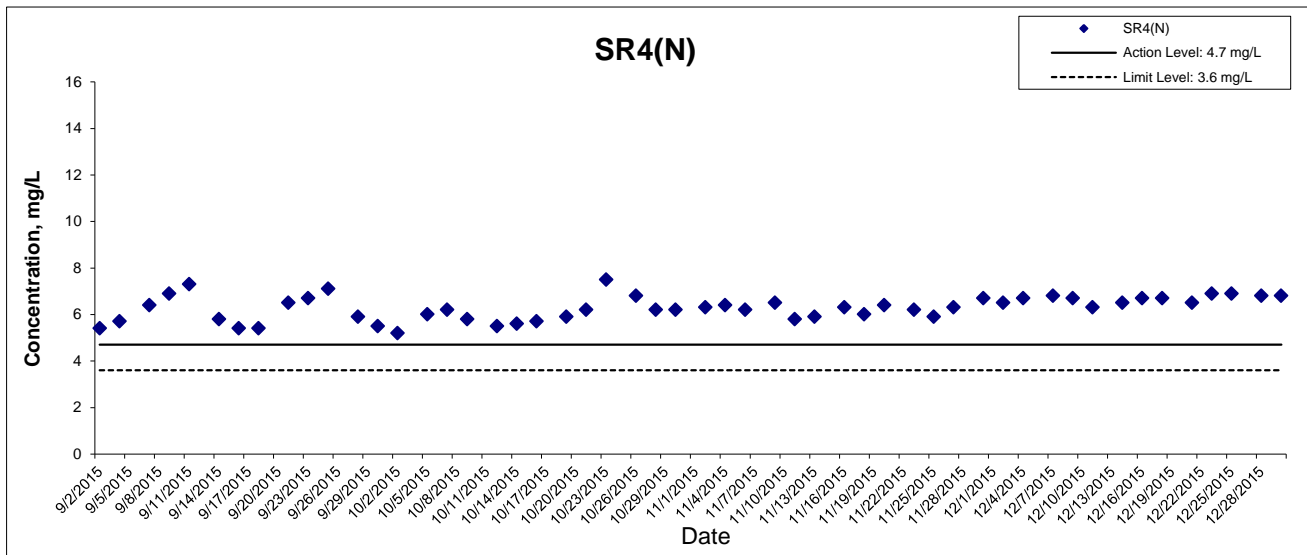


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

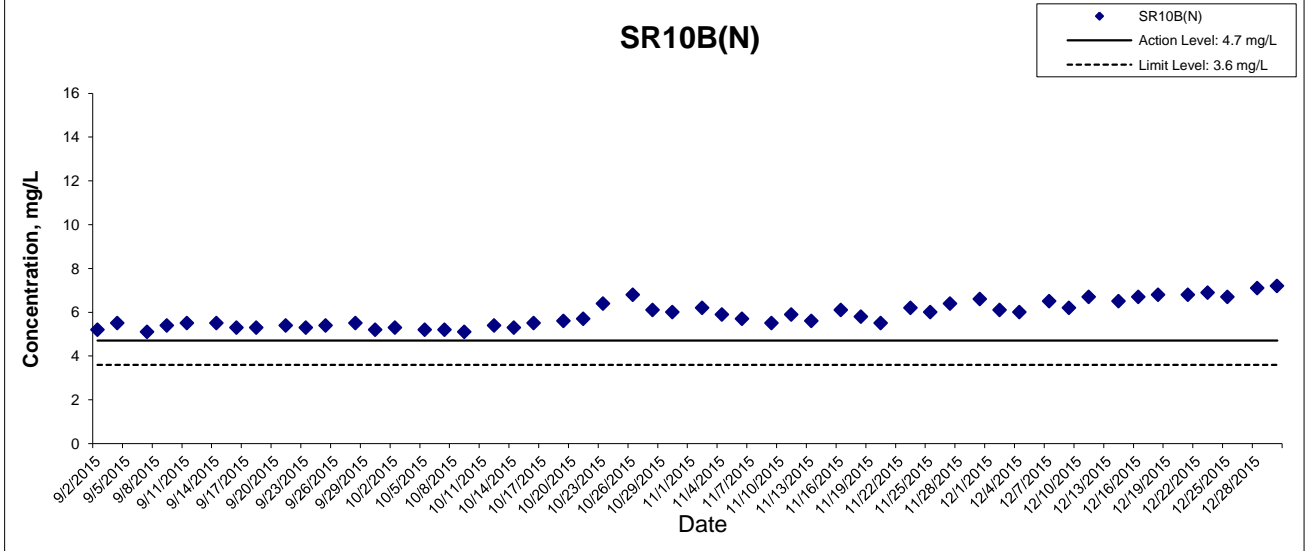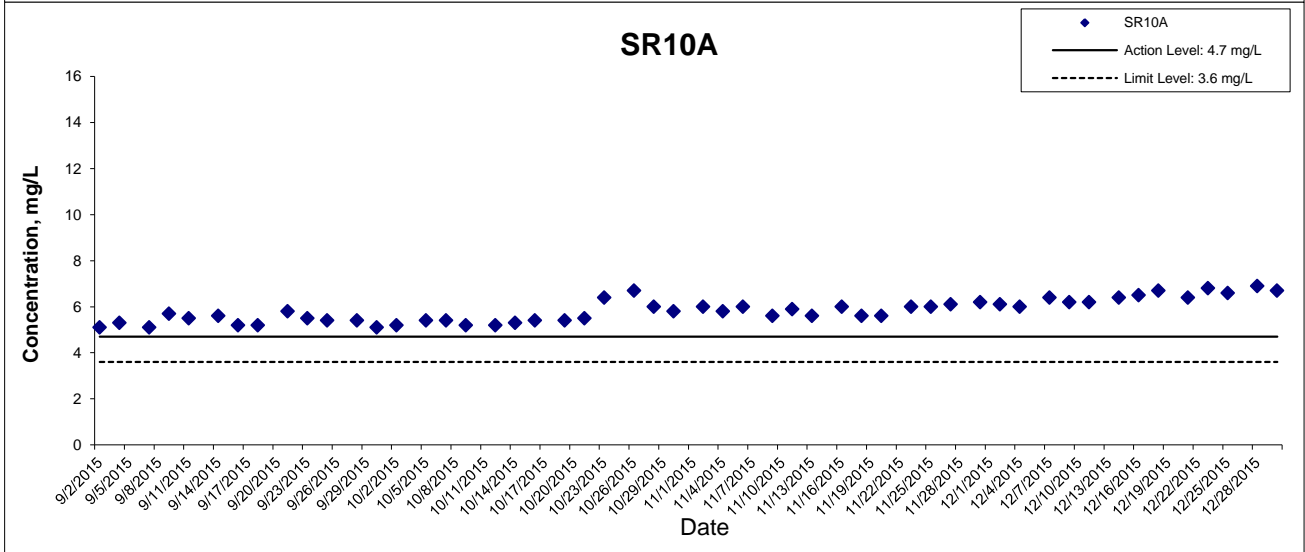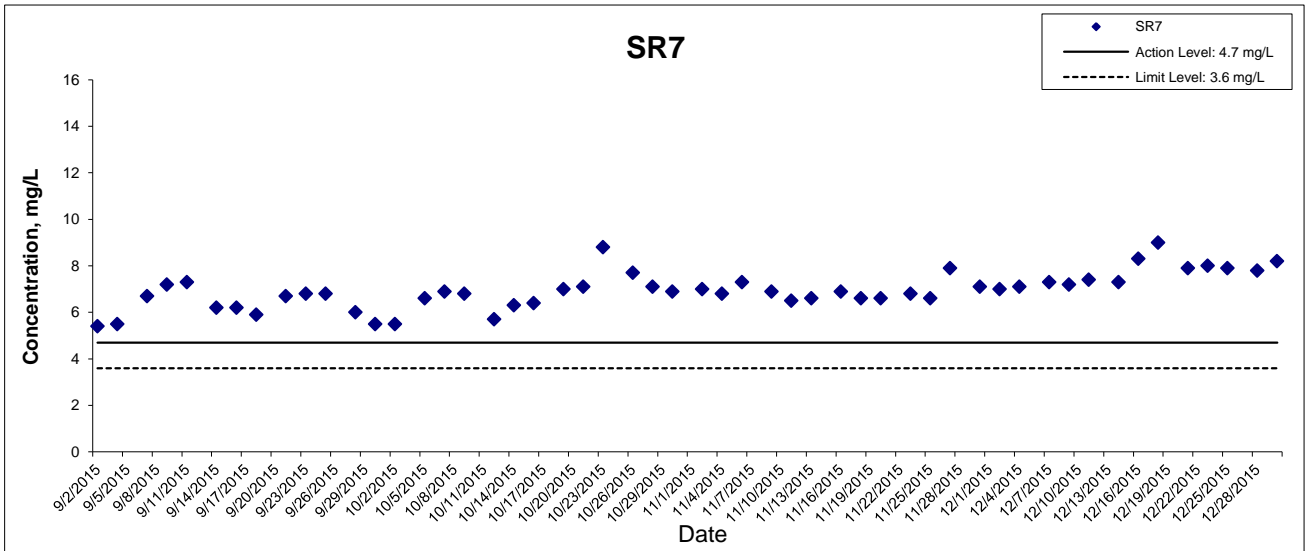




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

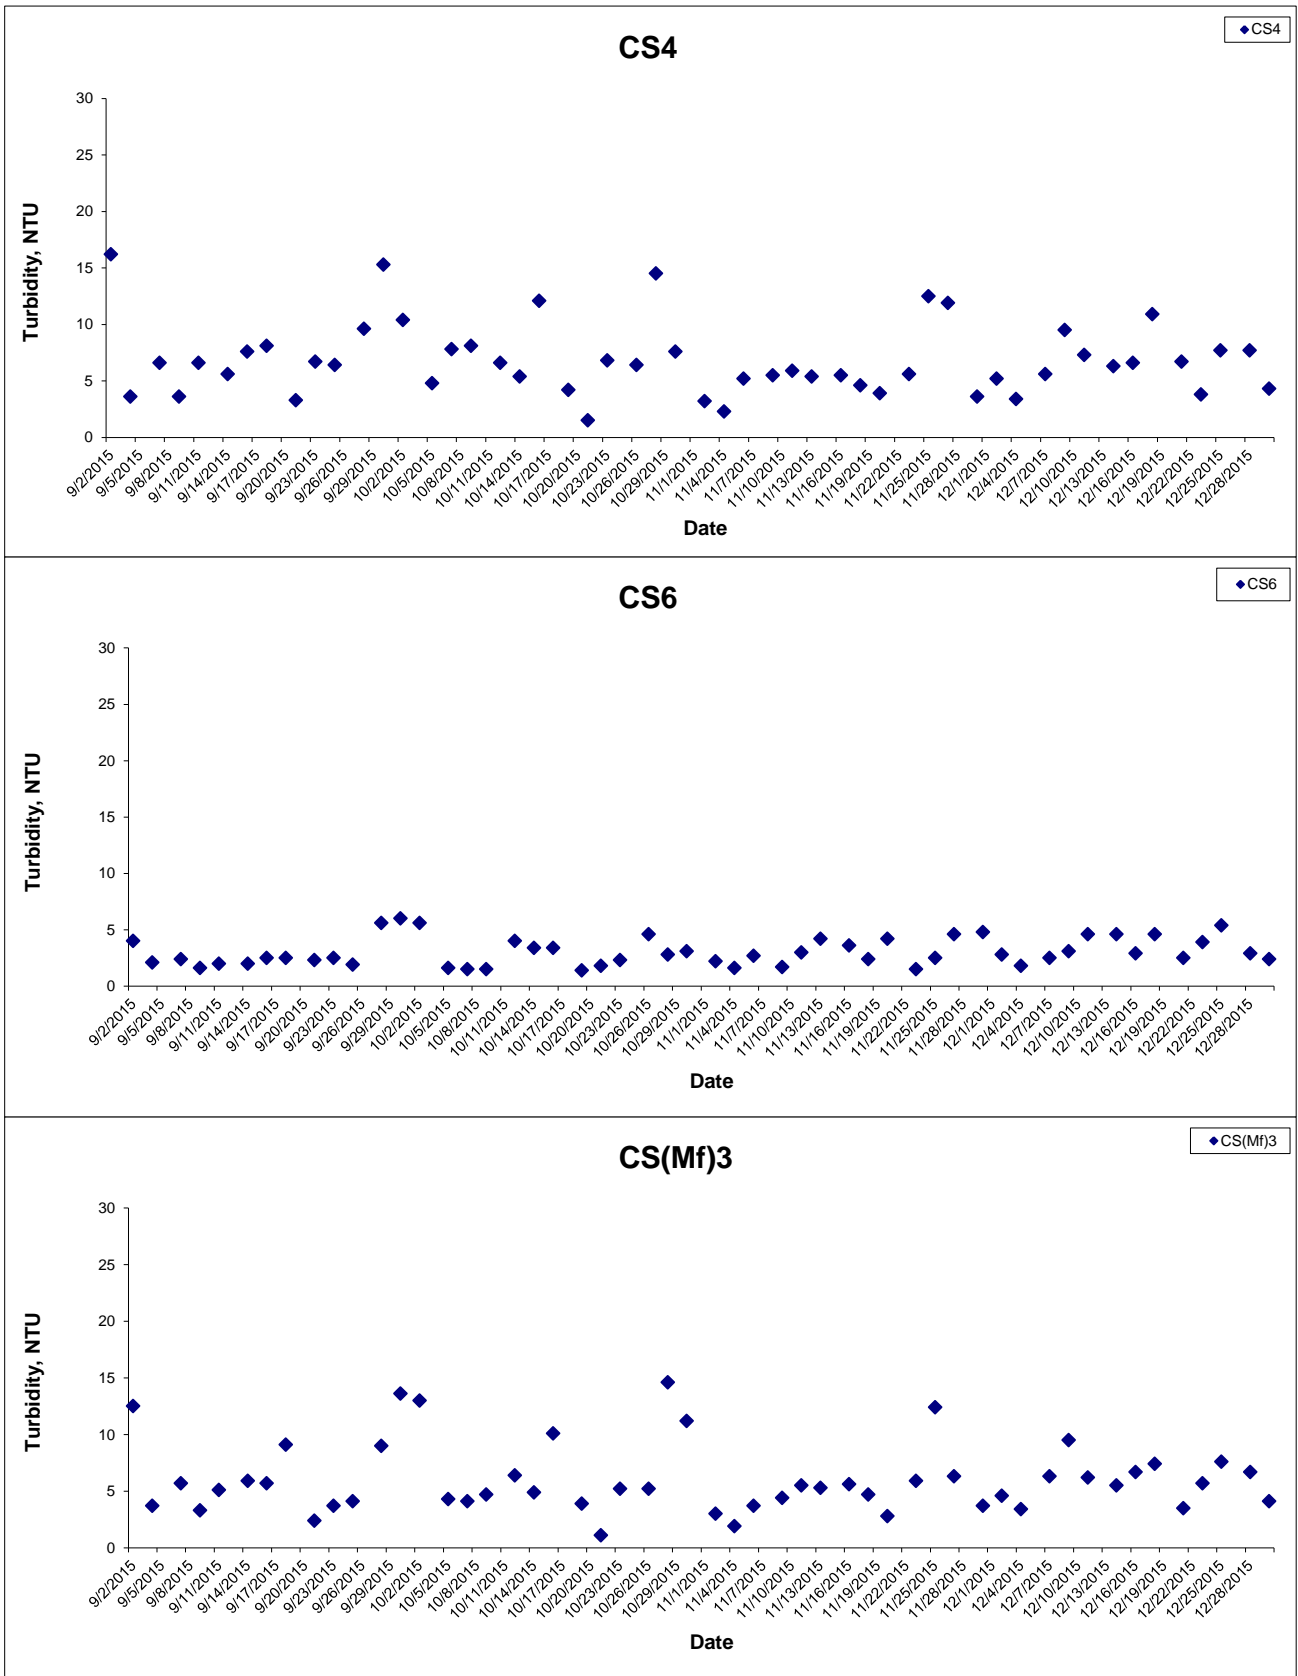

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Turbidity at Mid-Ebb Tide

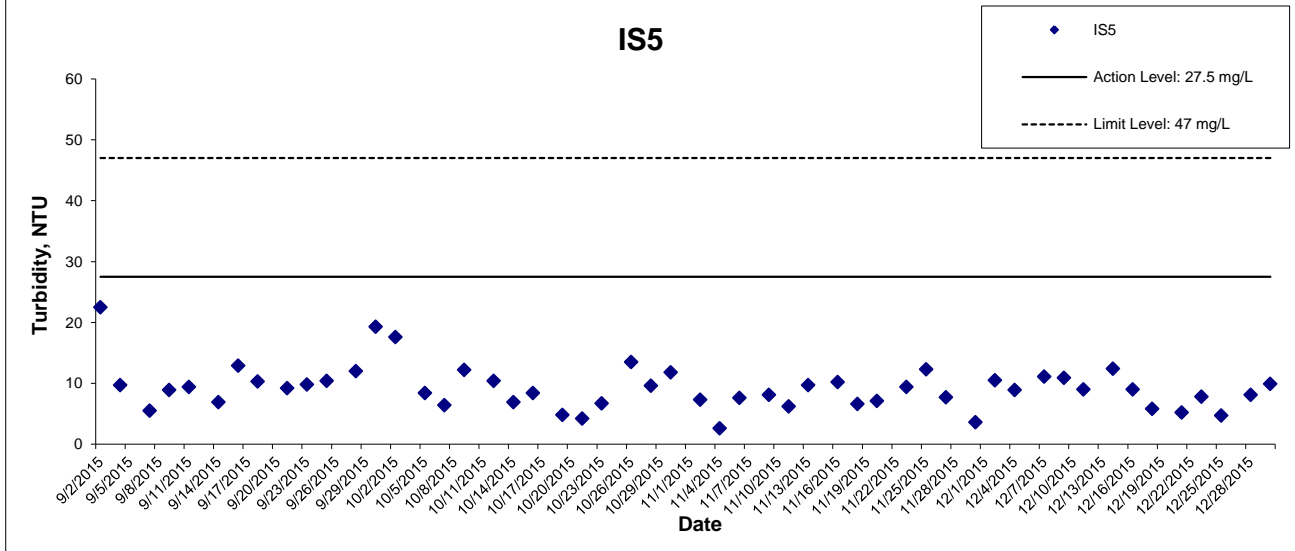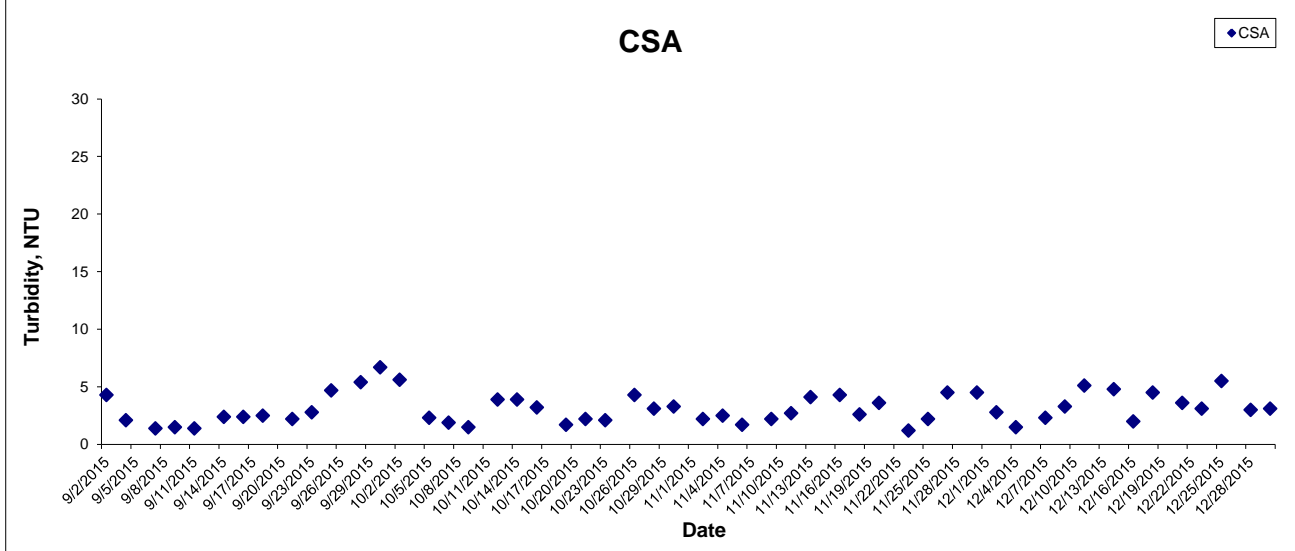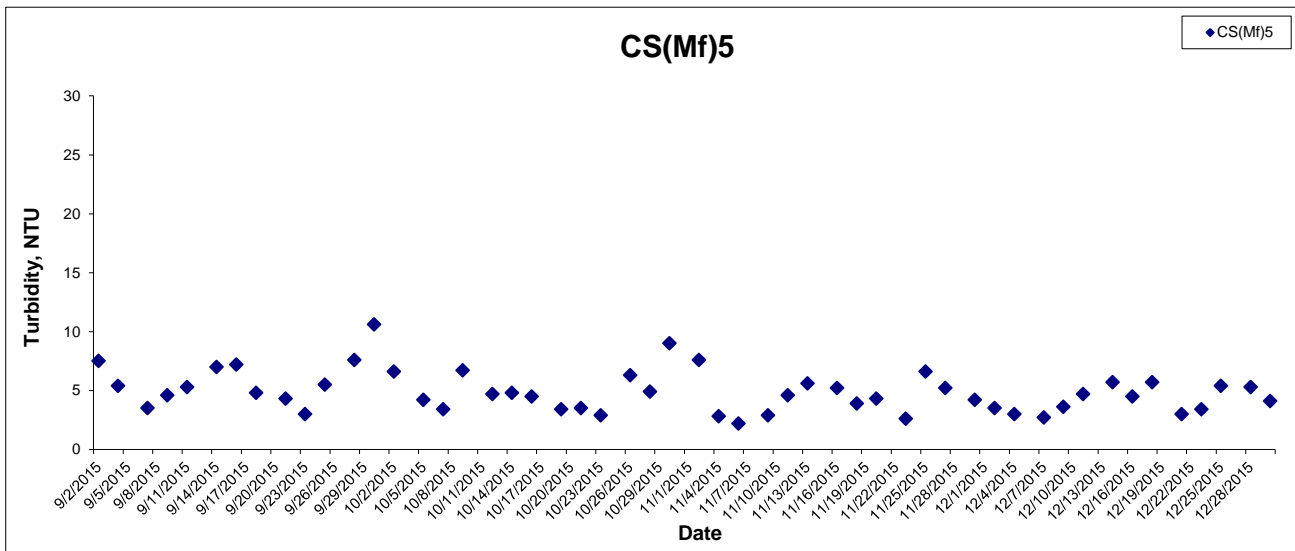

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Turbidity at Mid-Ebb Tide

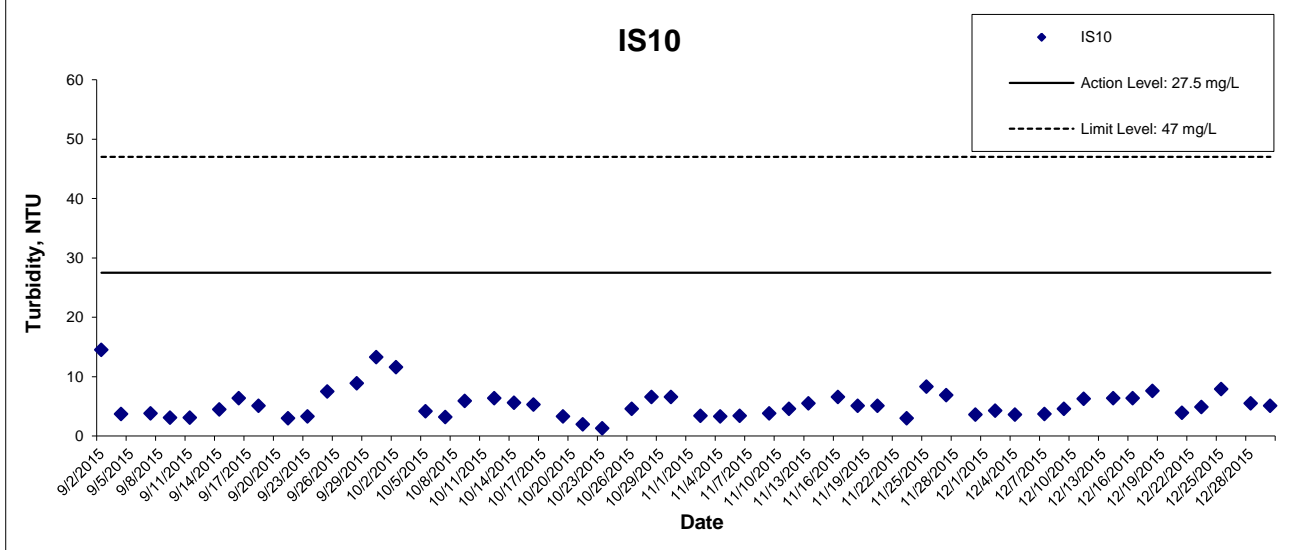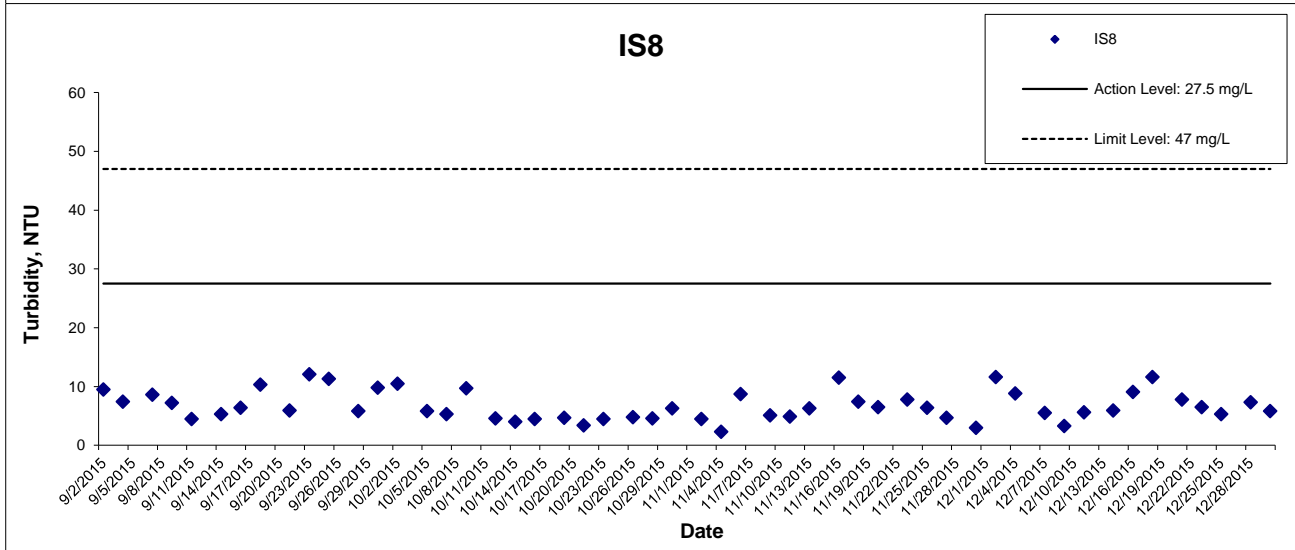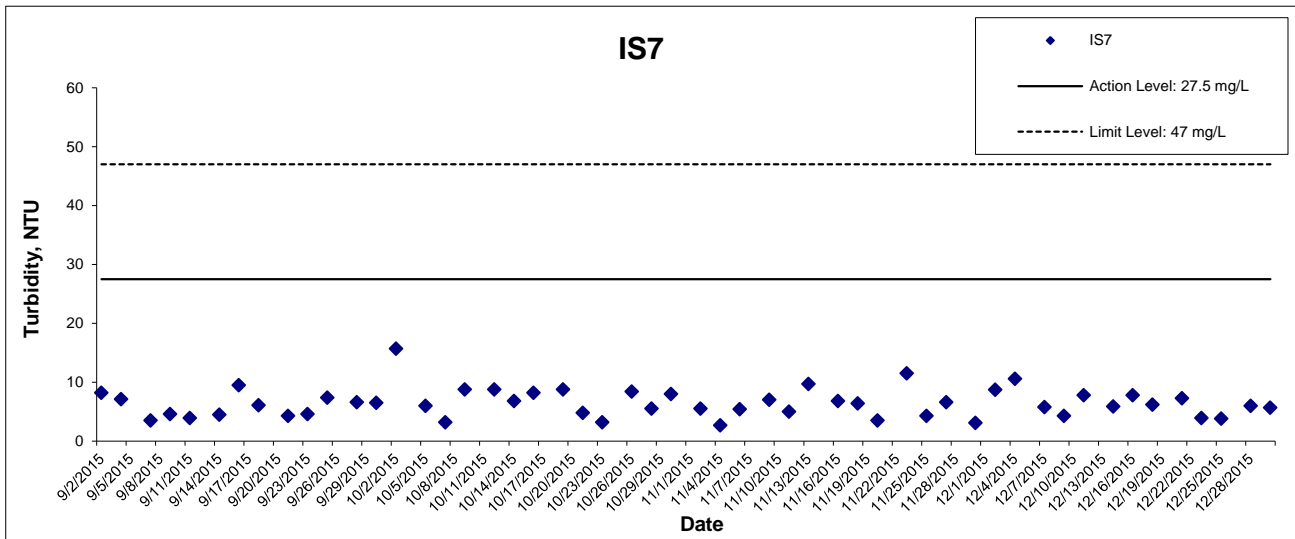

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Turbidity at Mid-Ebb Tide

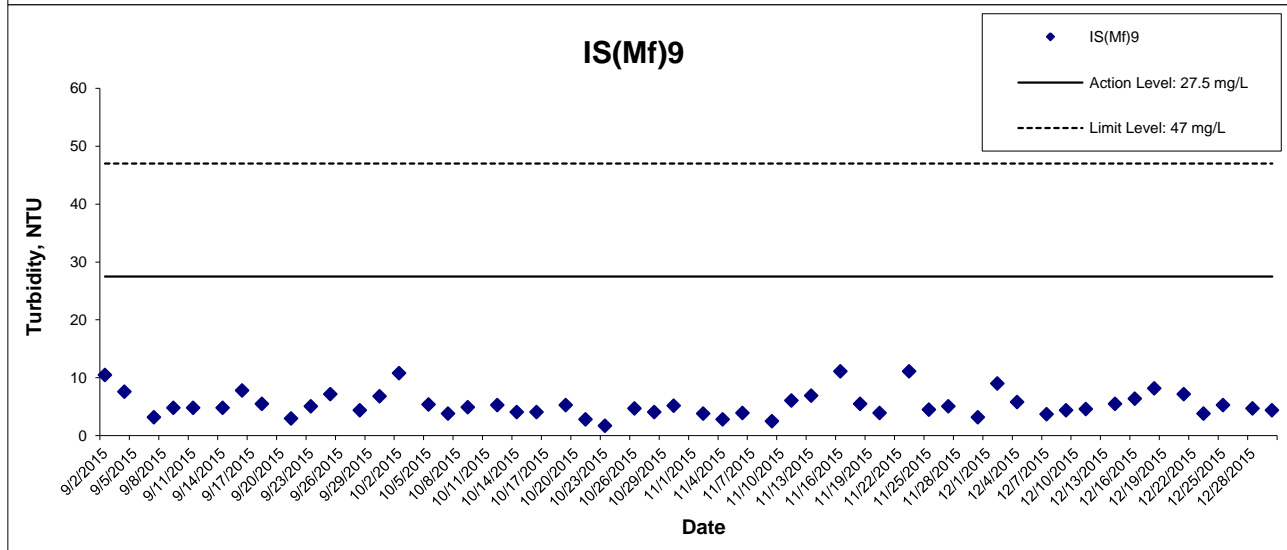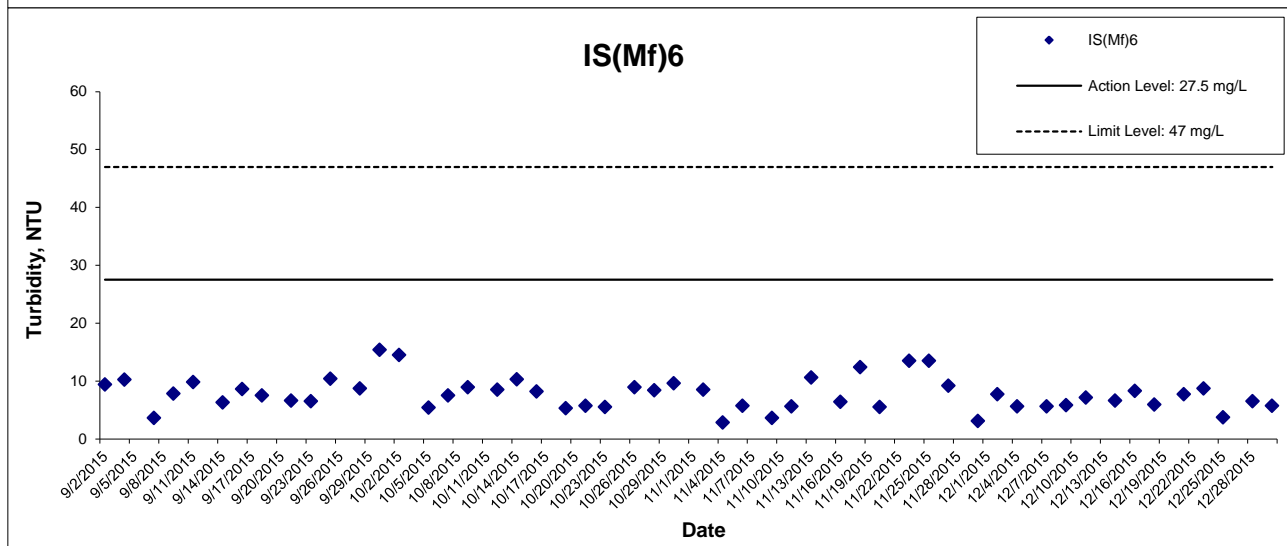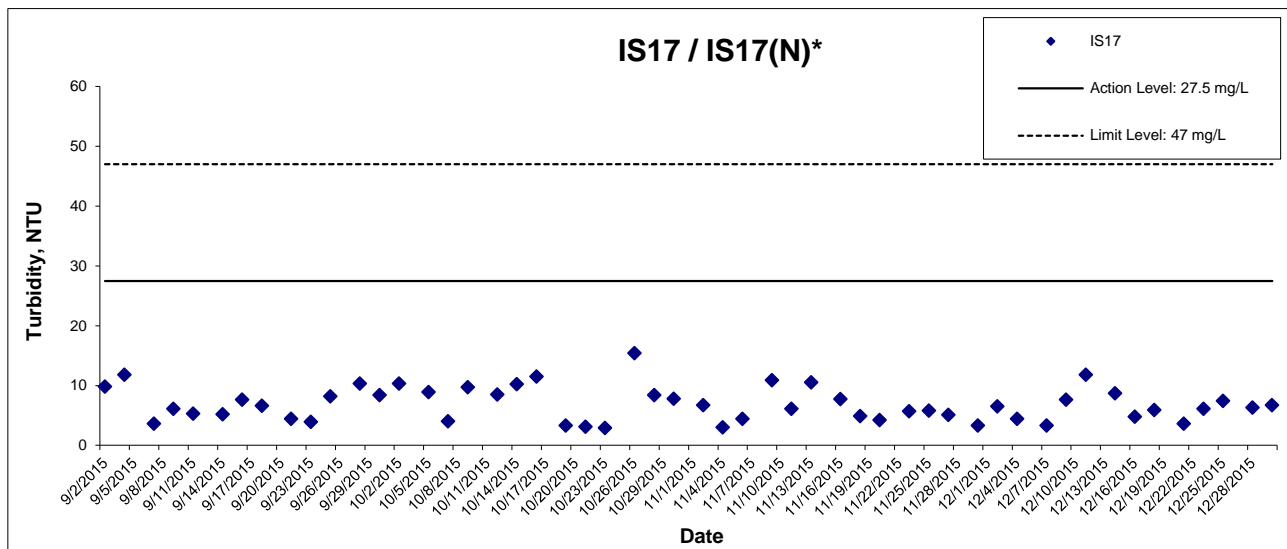


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

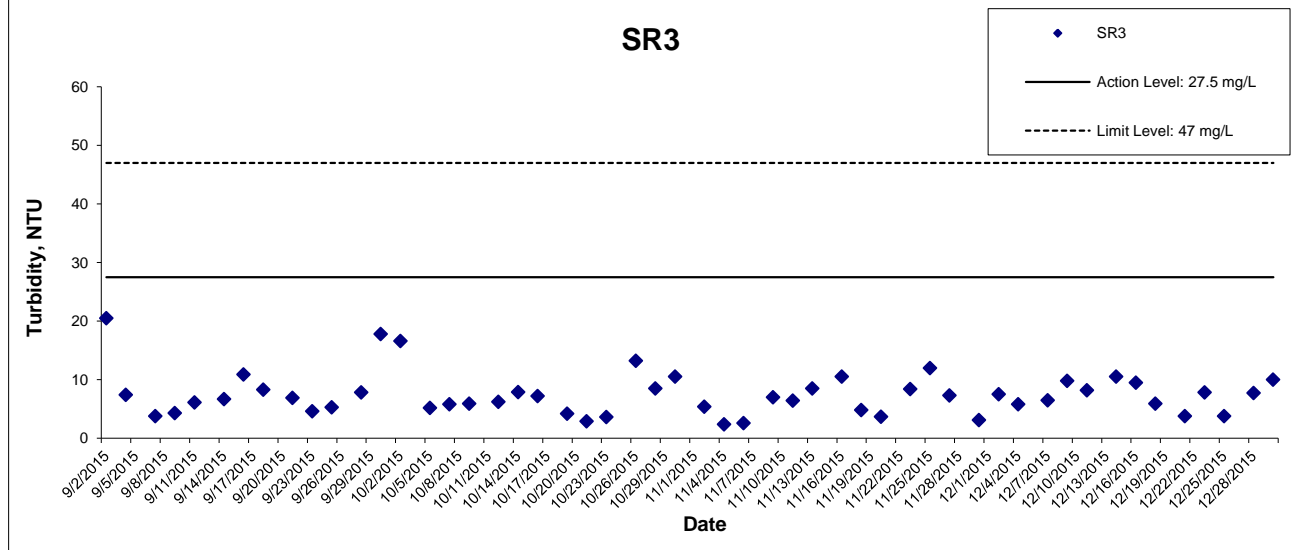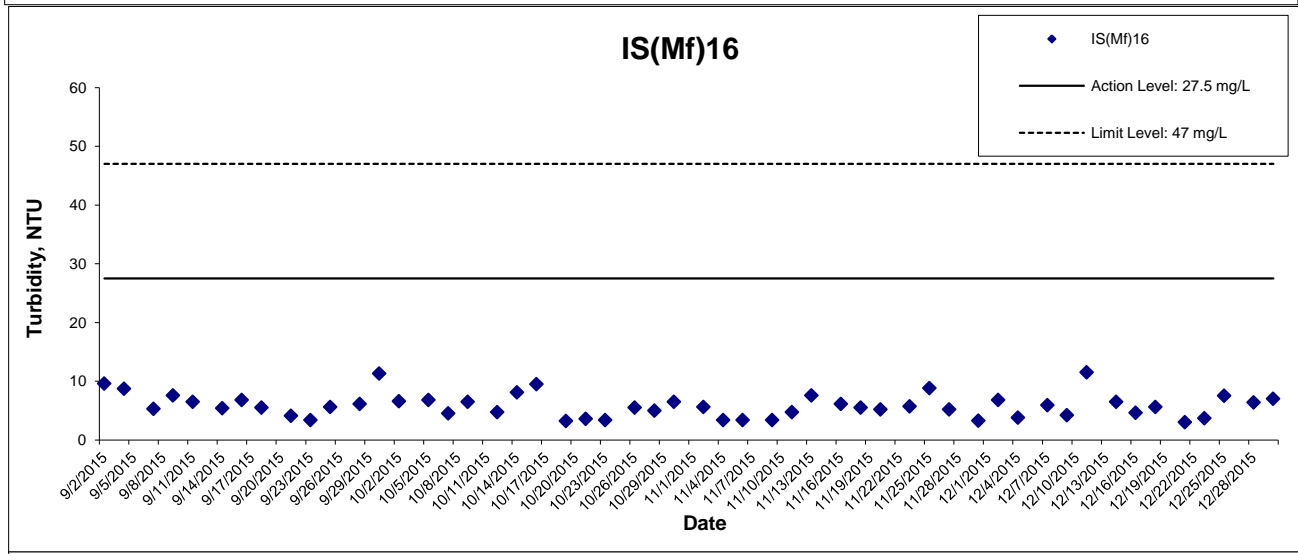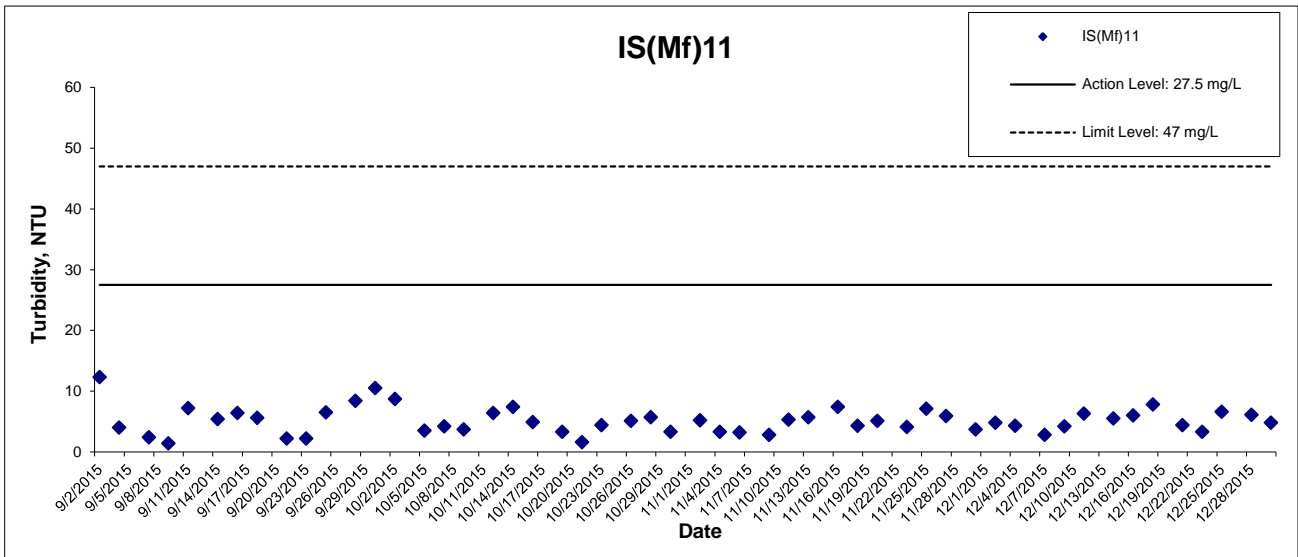




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

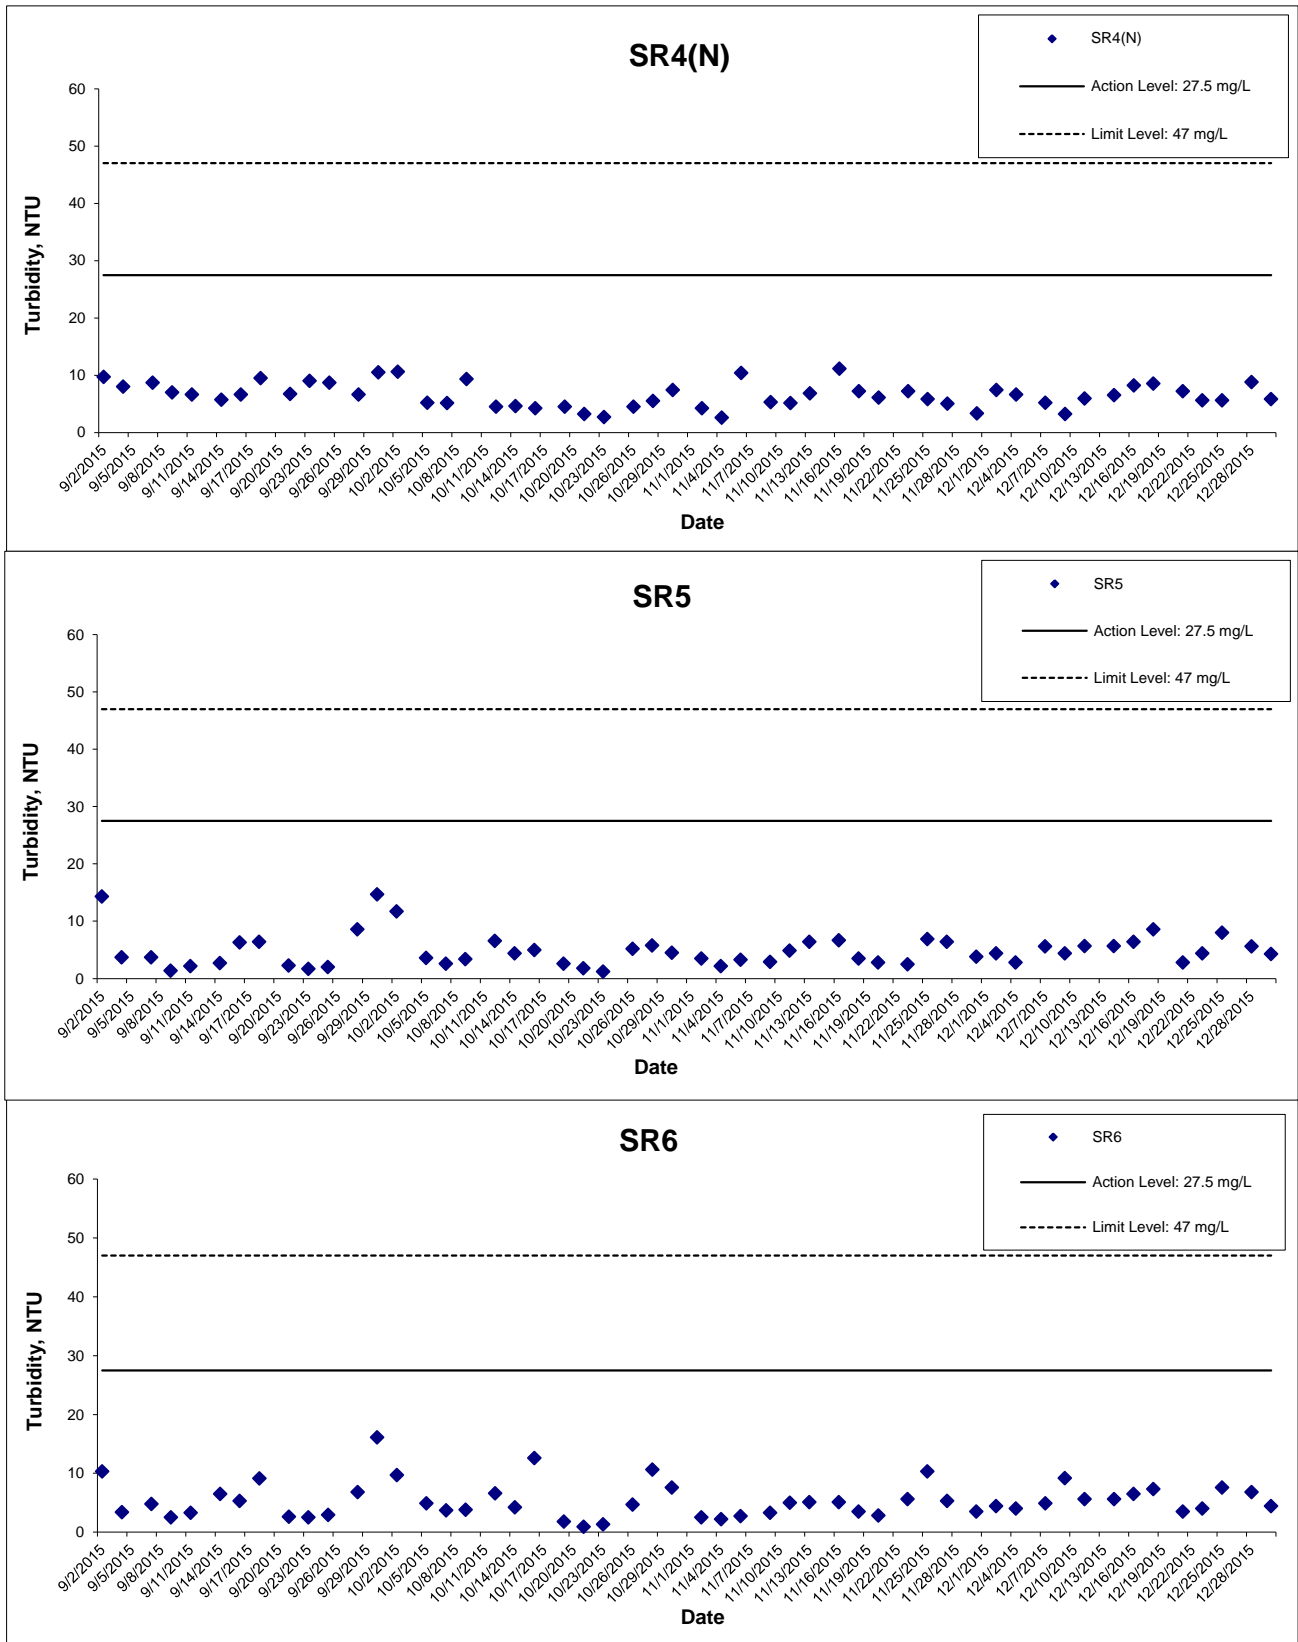

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Turbidity at Mid-Ebb Tide

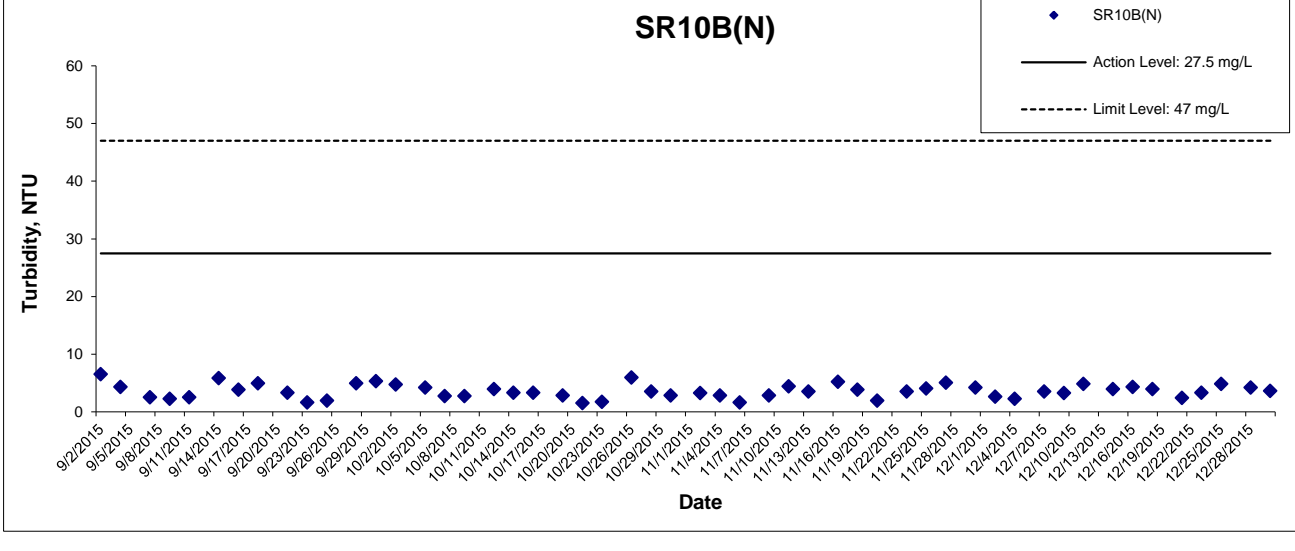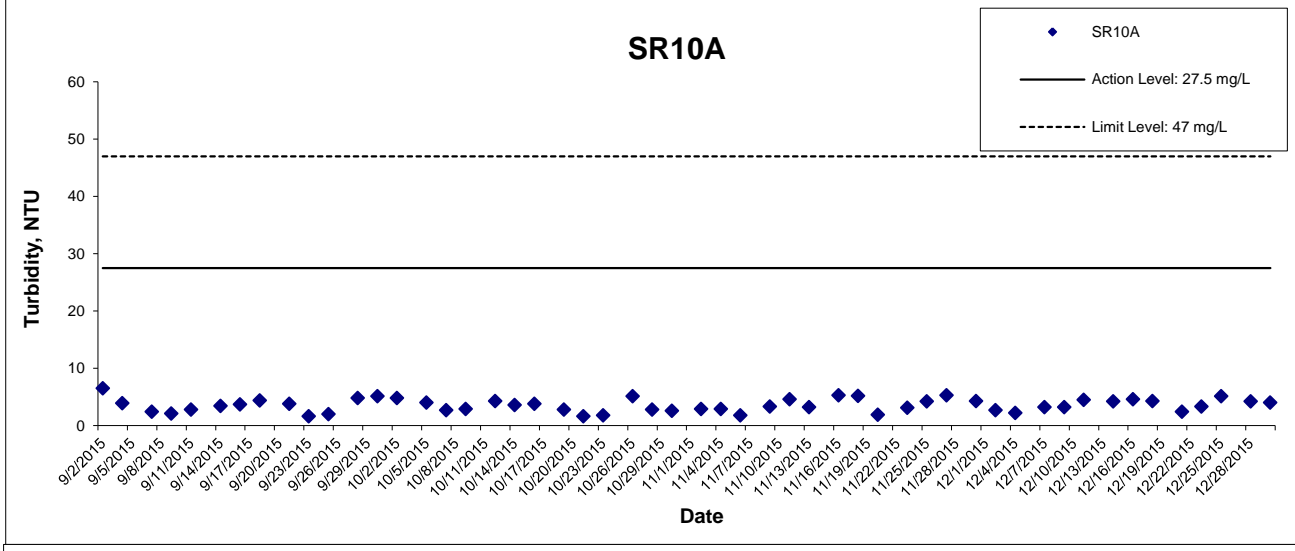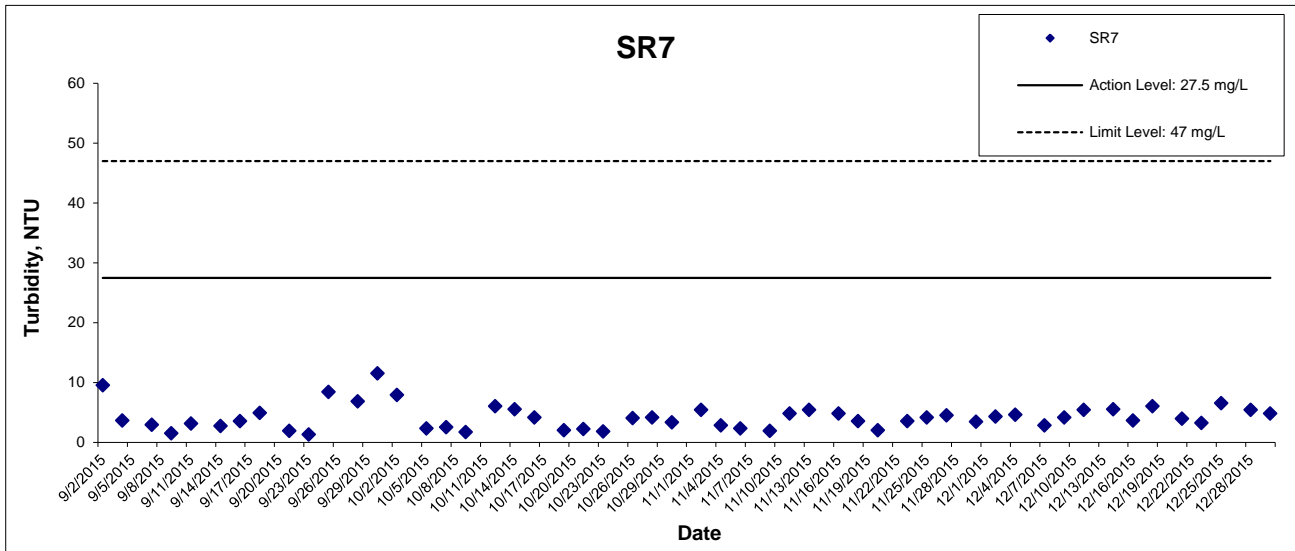

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Turbidity at Mid-Flood Tide

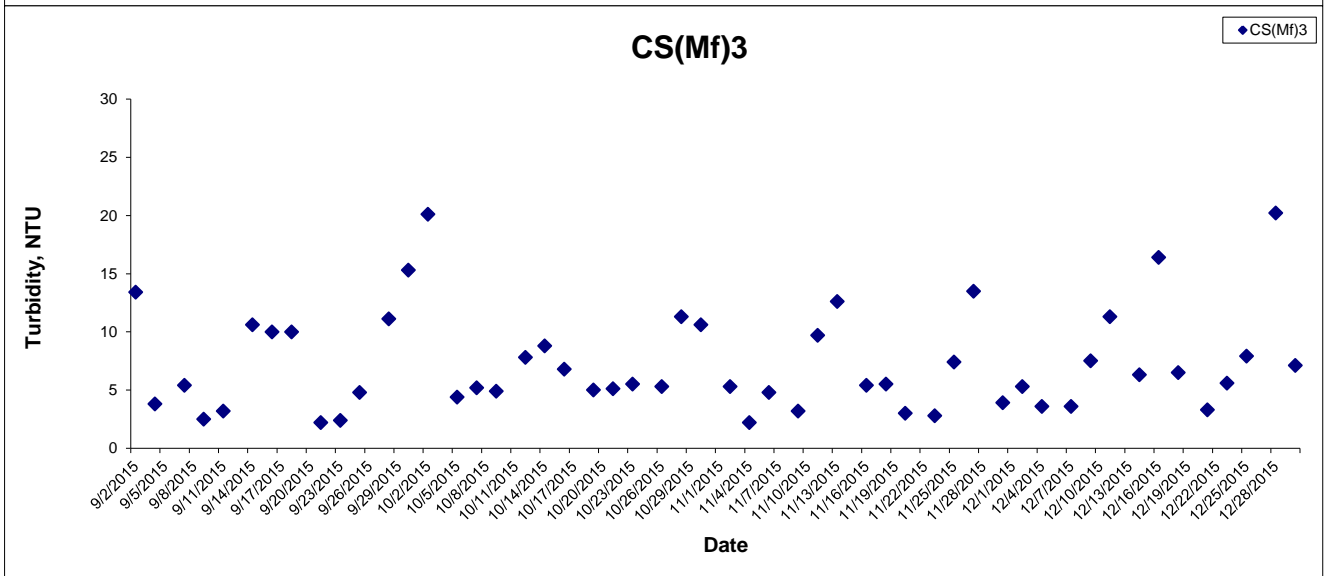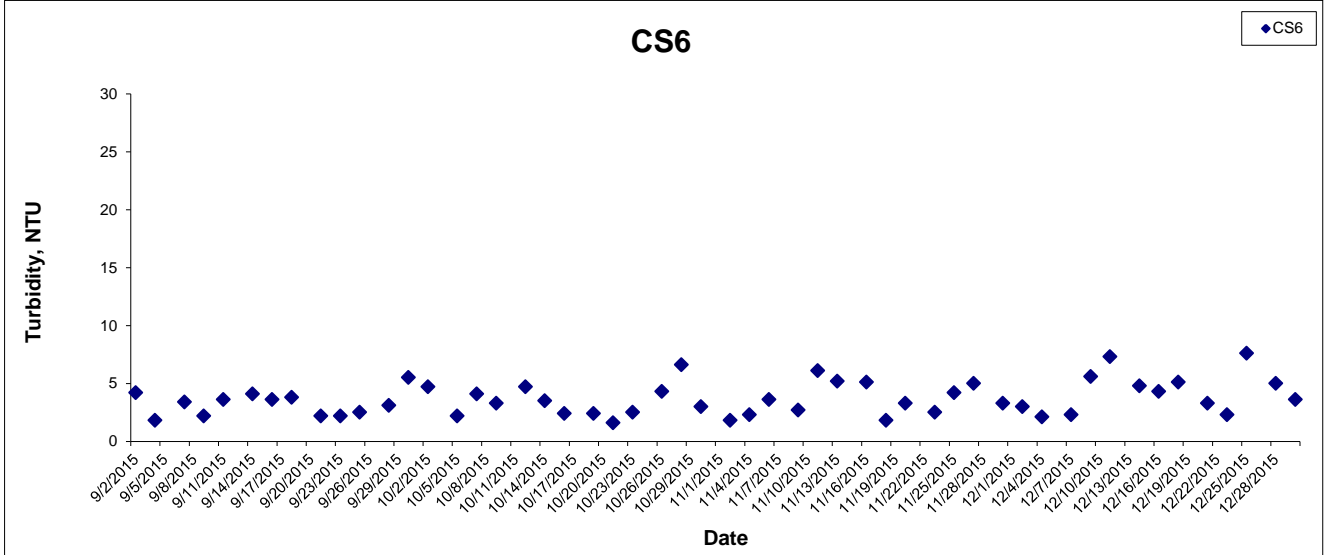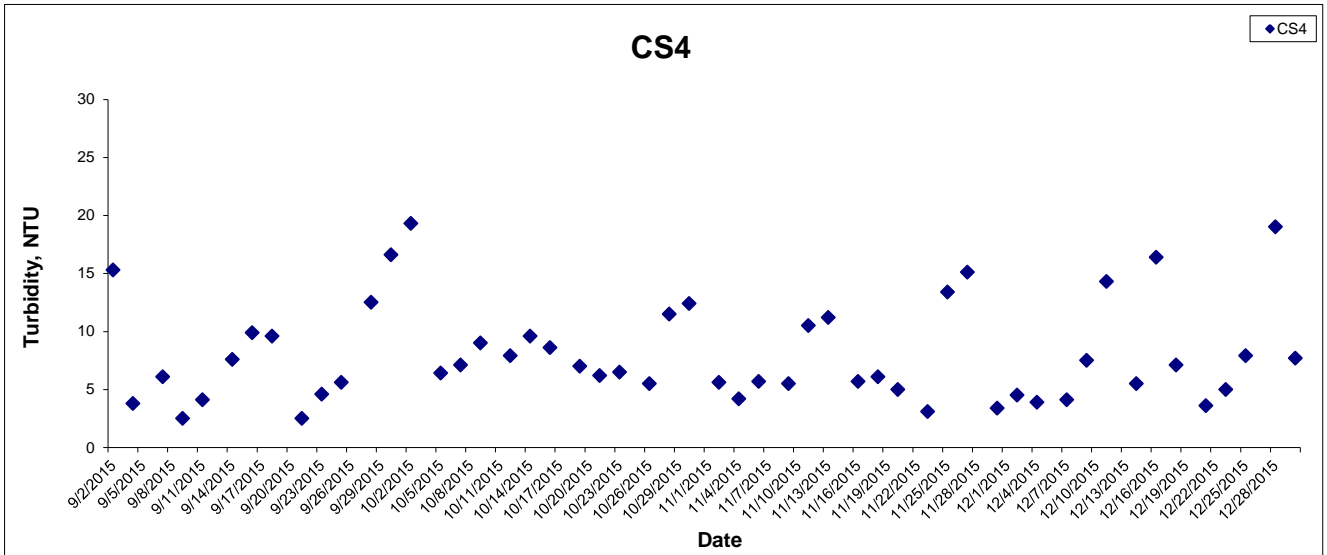




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

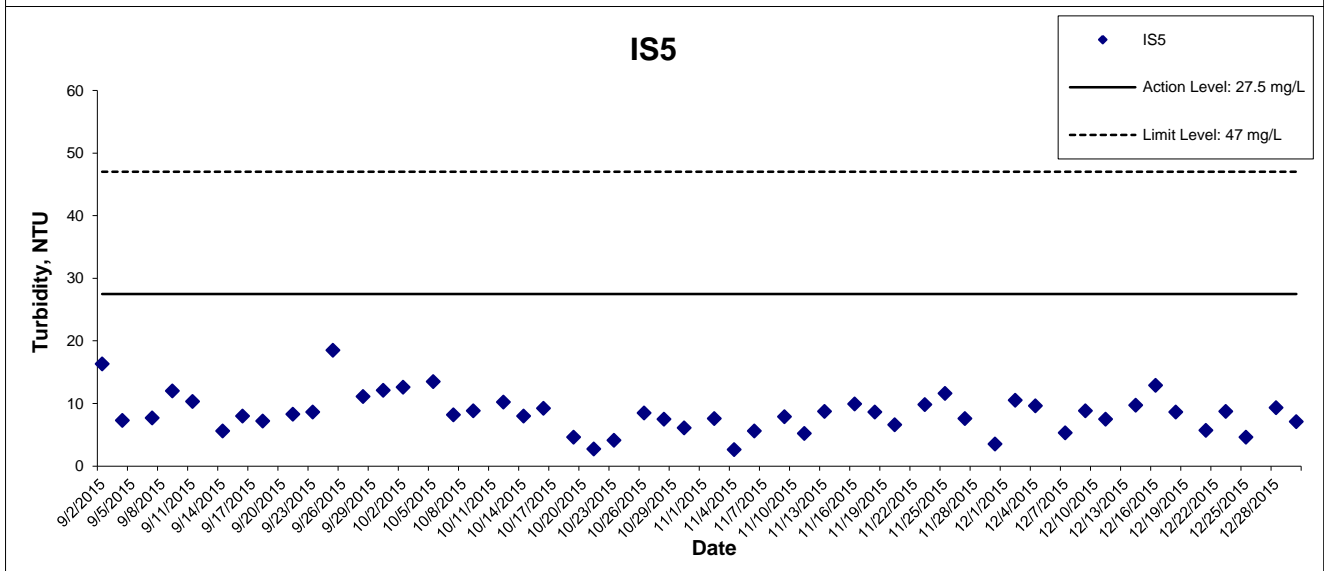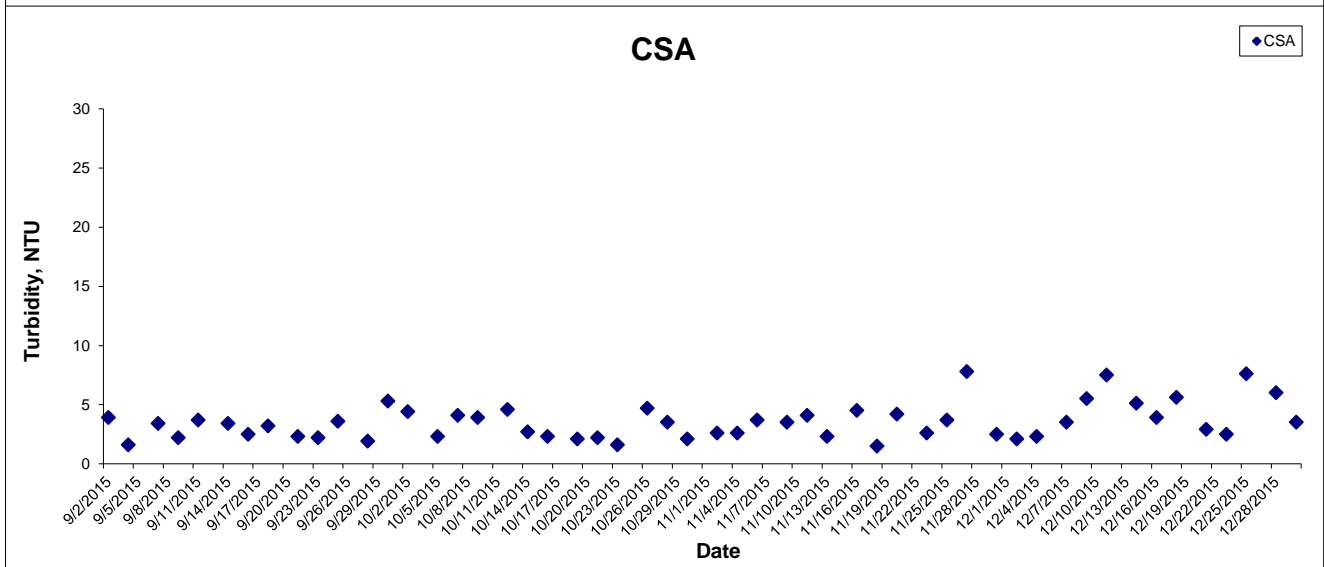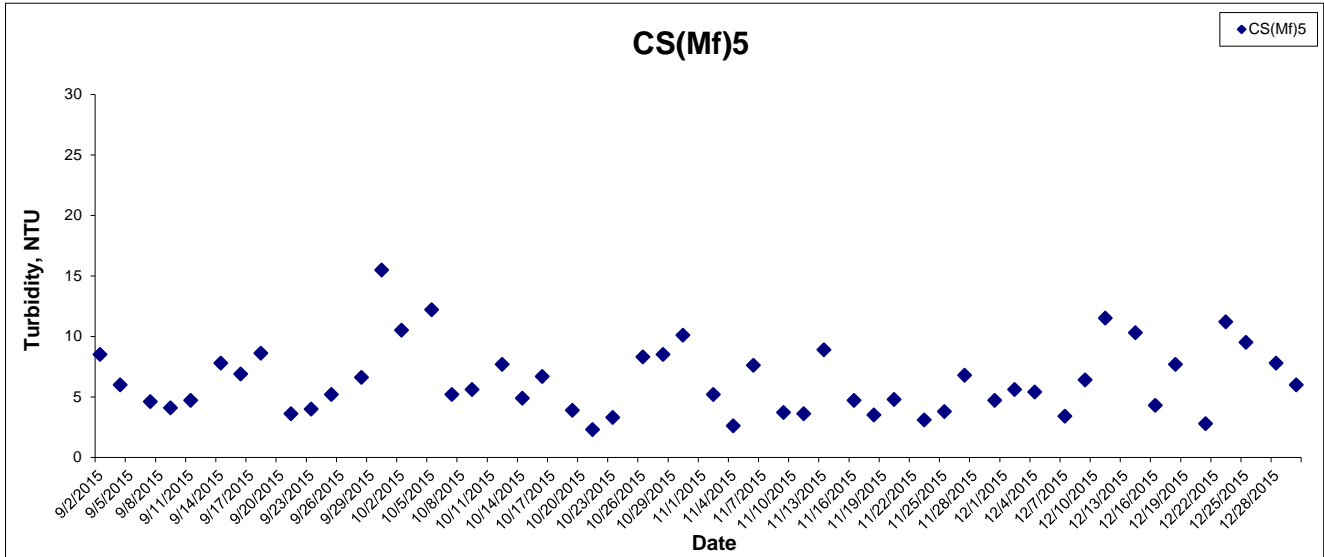




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

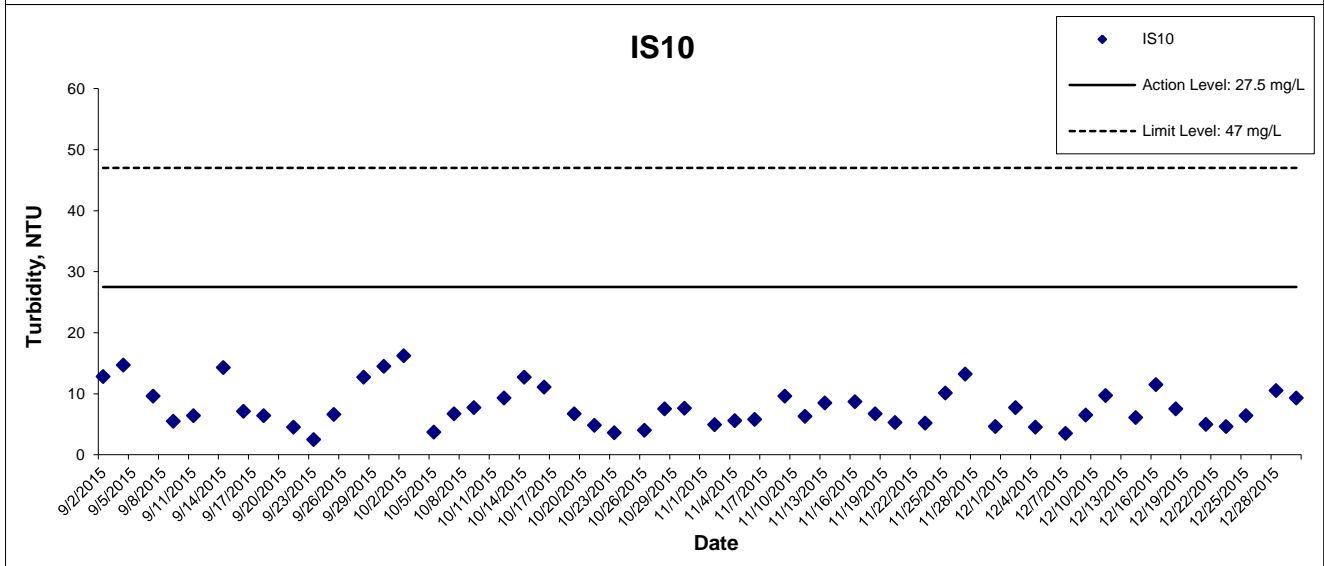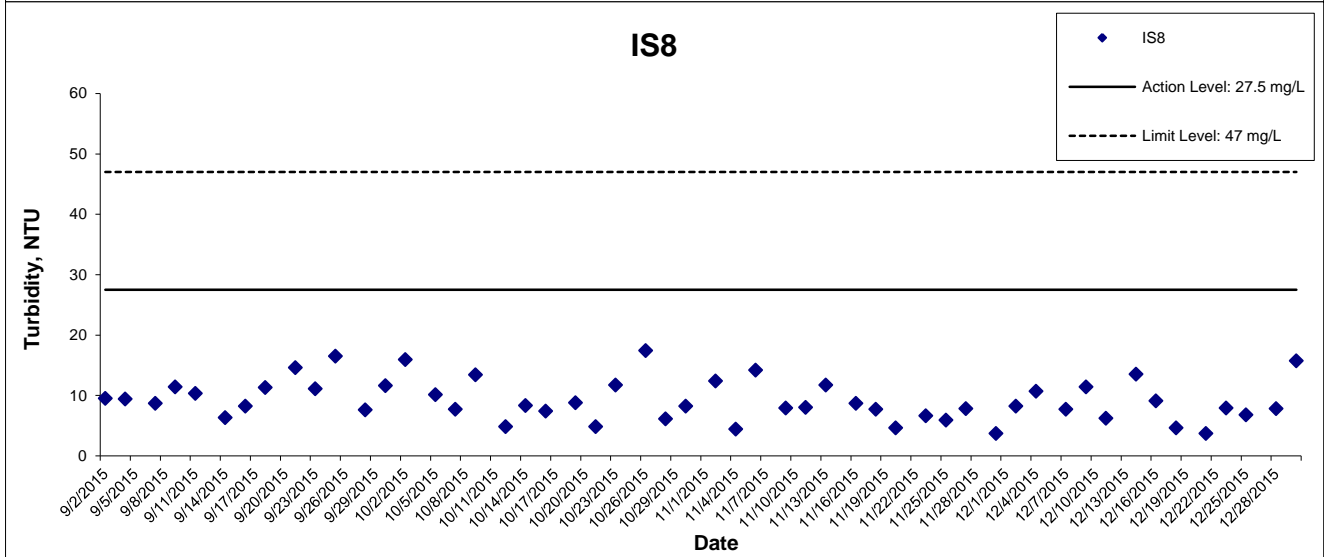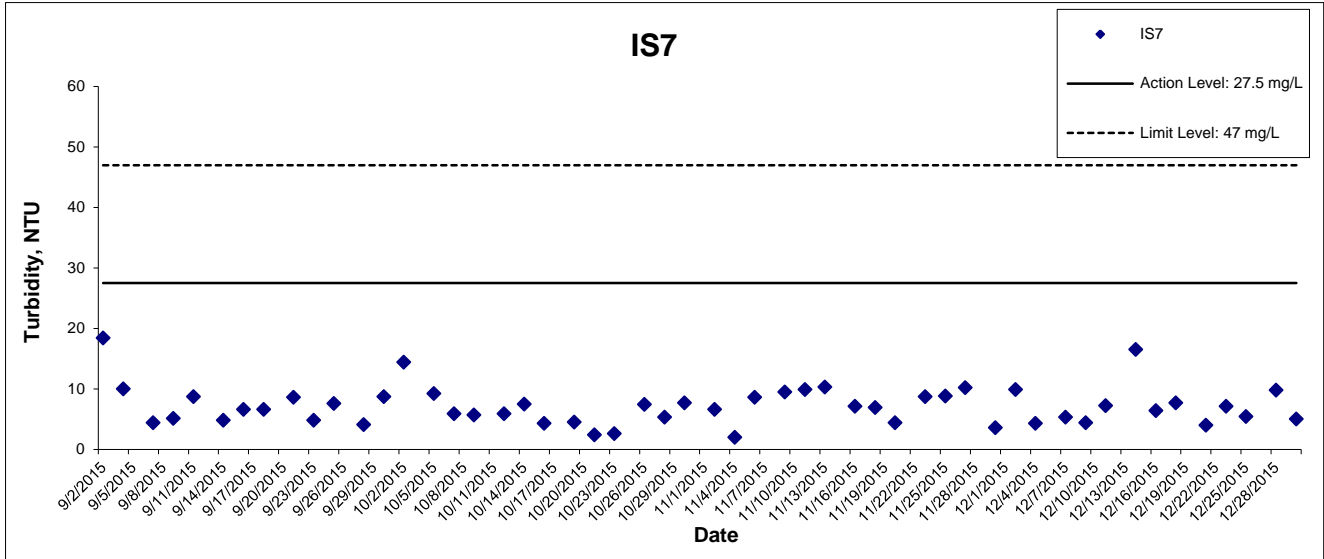




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

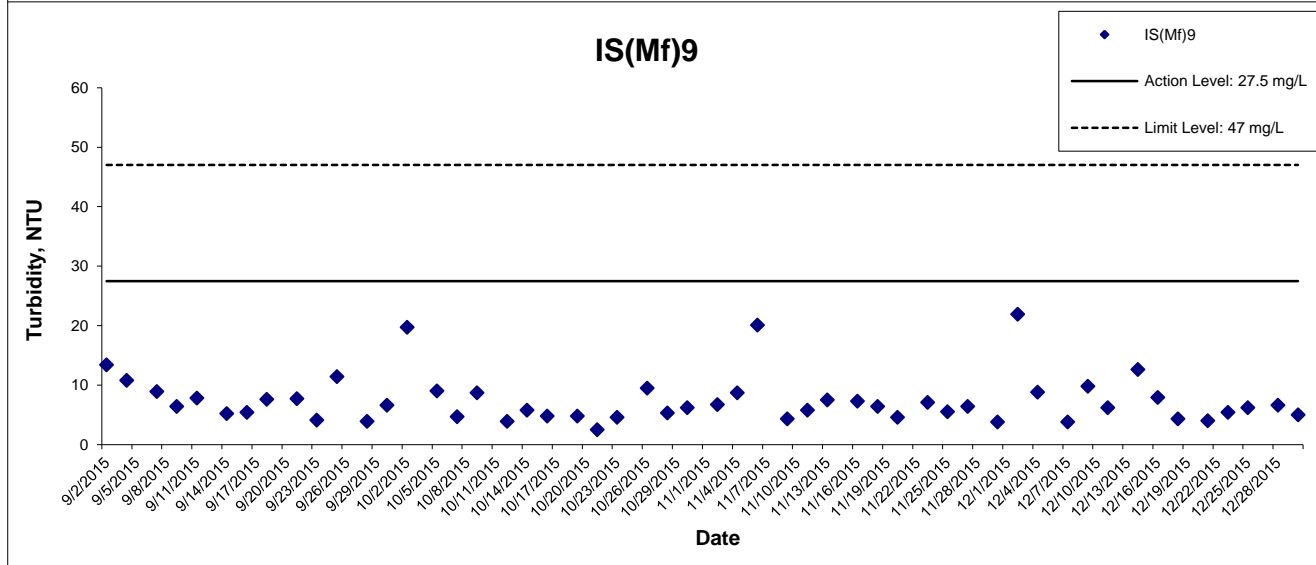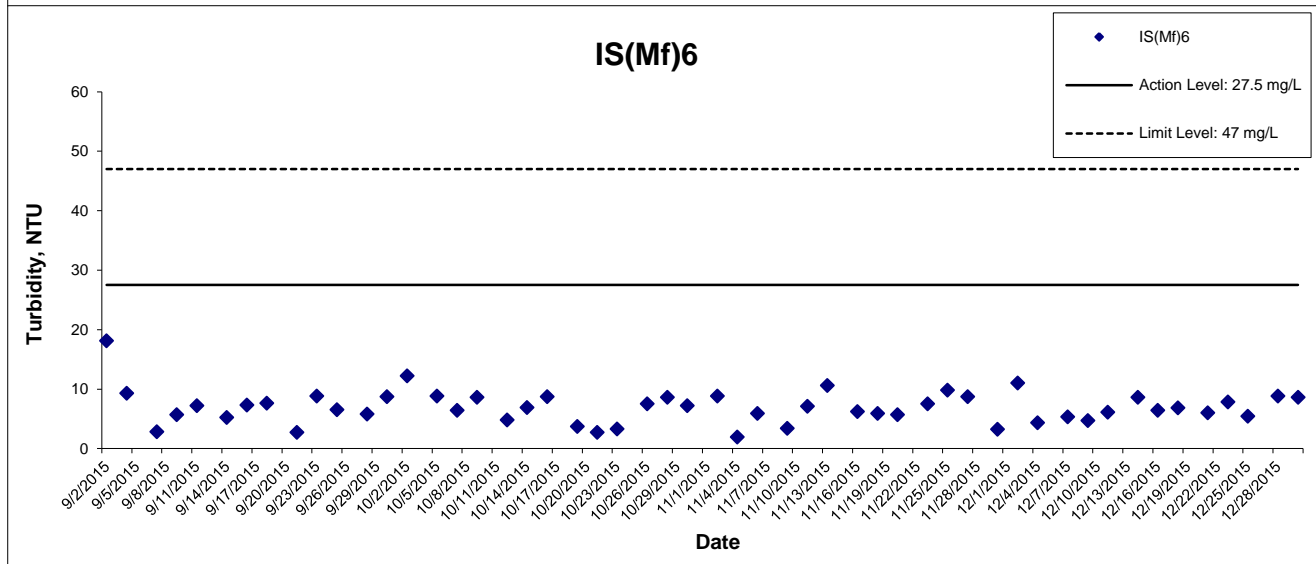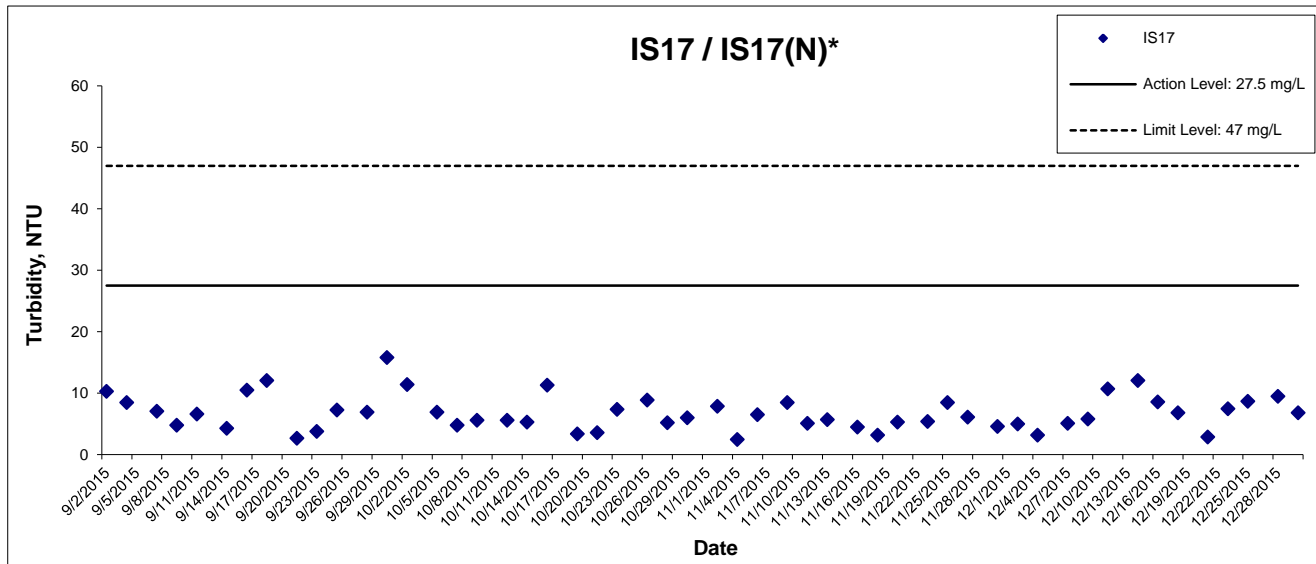

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

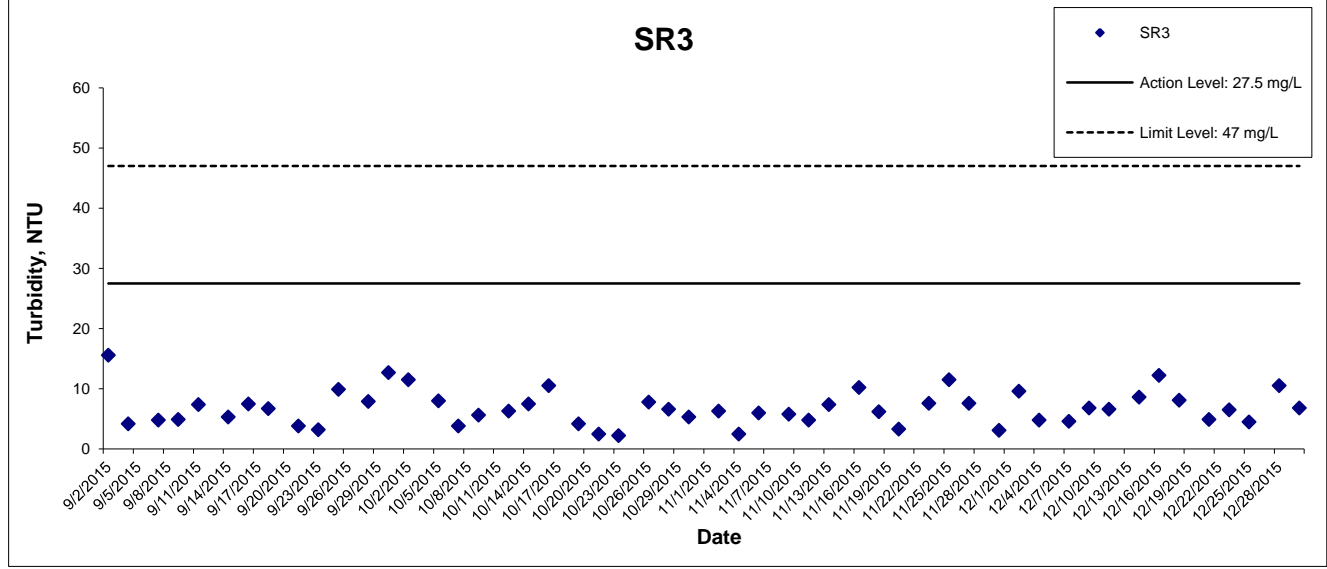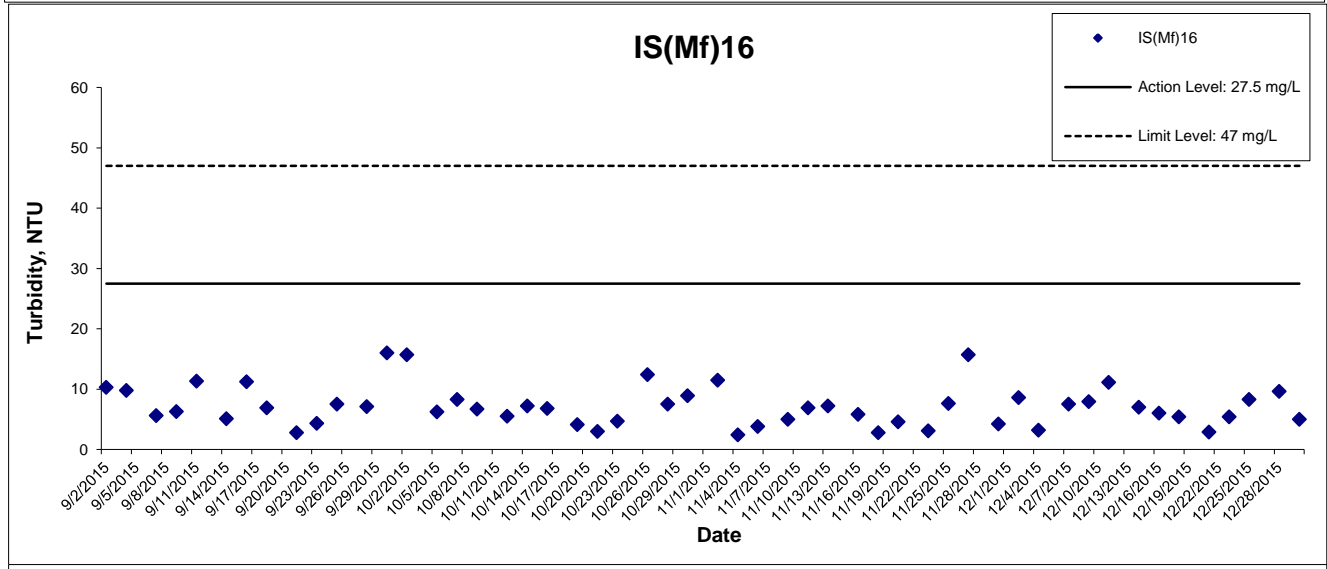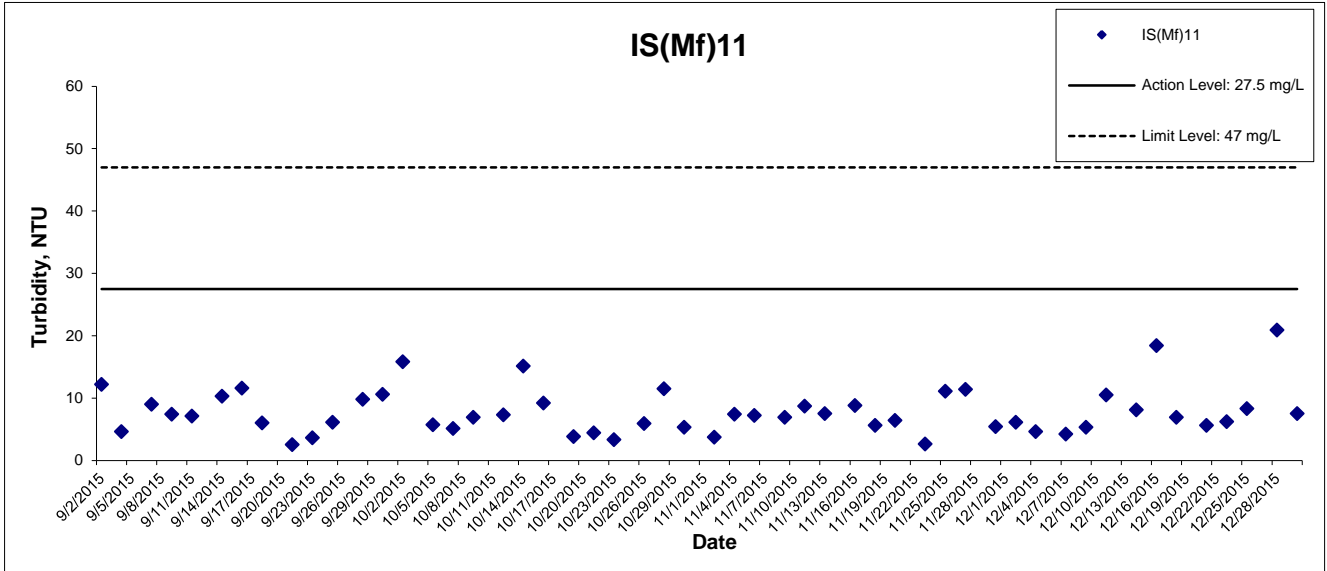

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE




HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results



Turbidity at Mid-Flood Tide

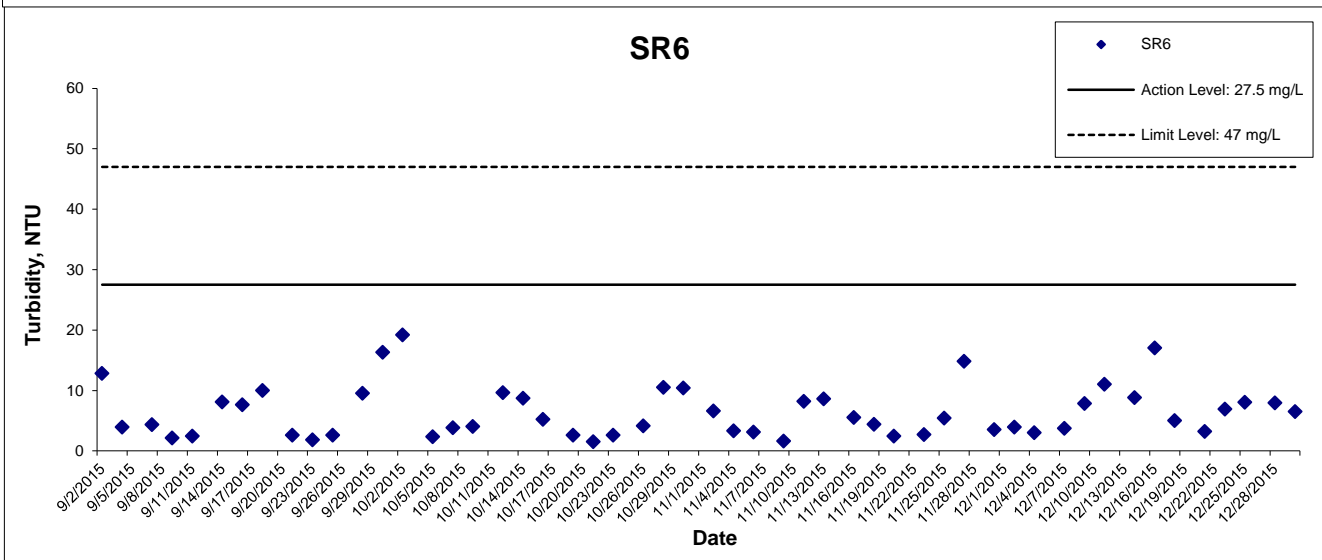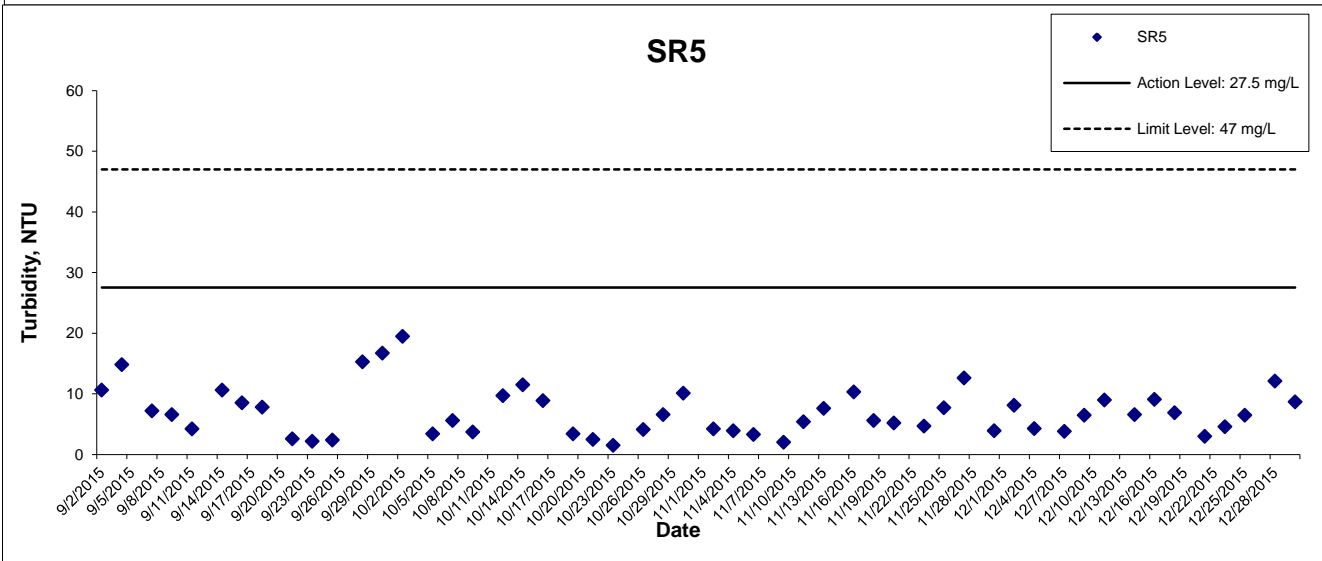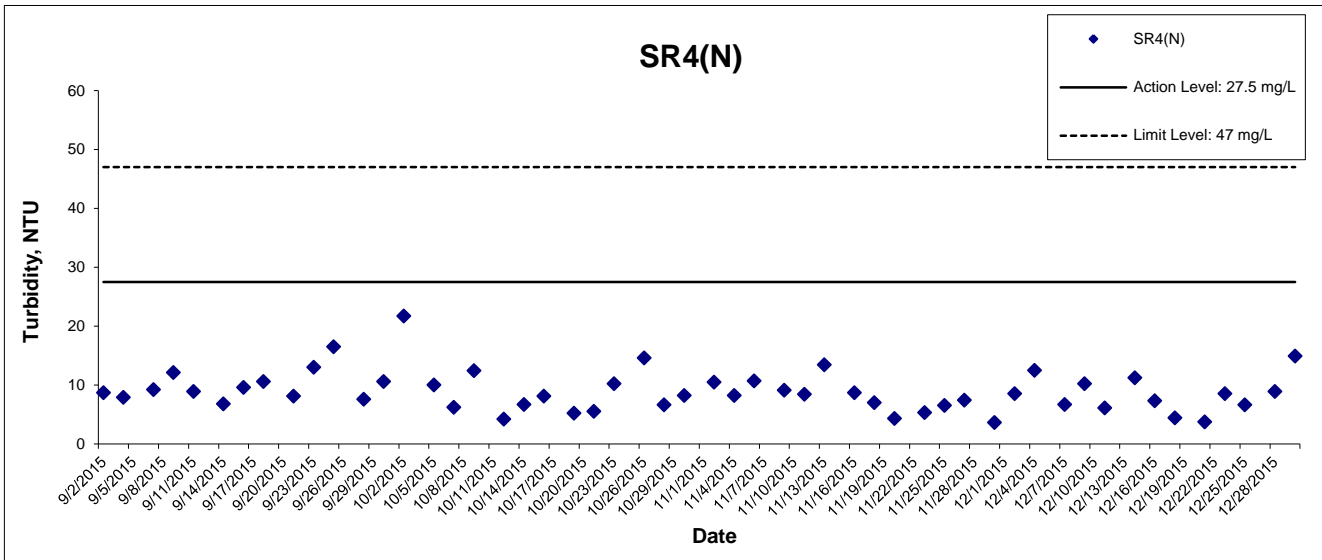

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE




HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**






Turbidity at Mid-Flood Tide

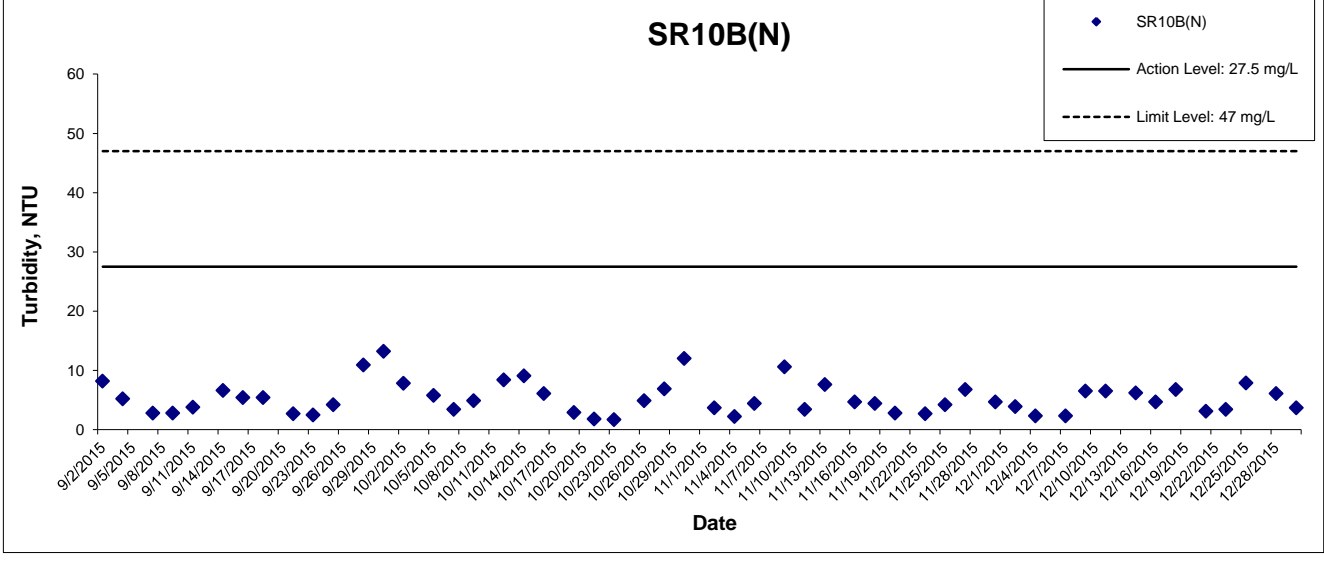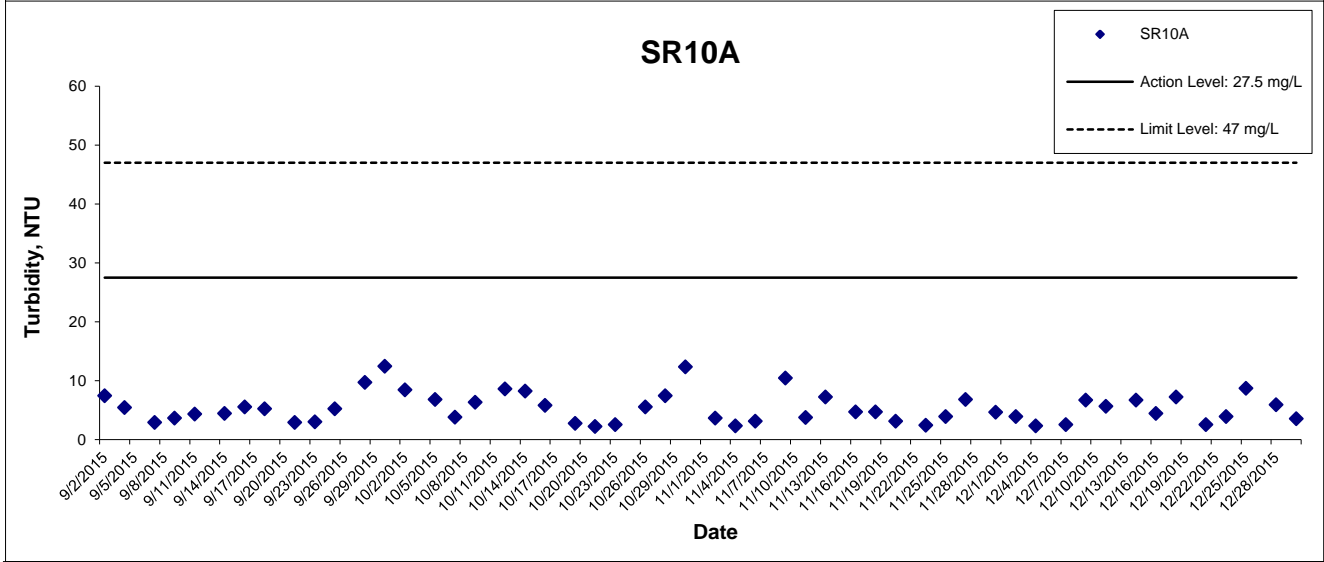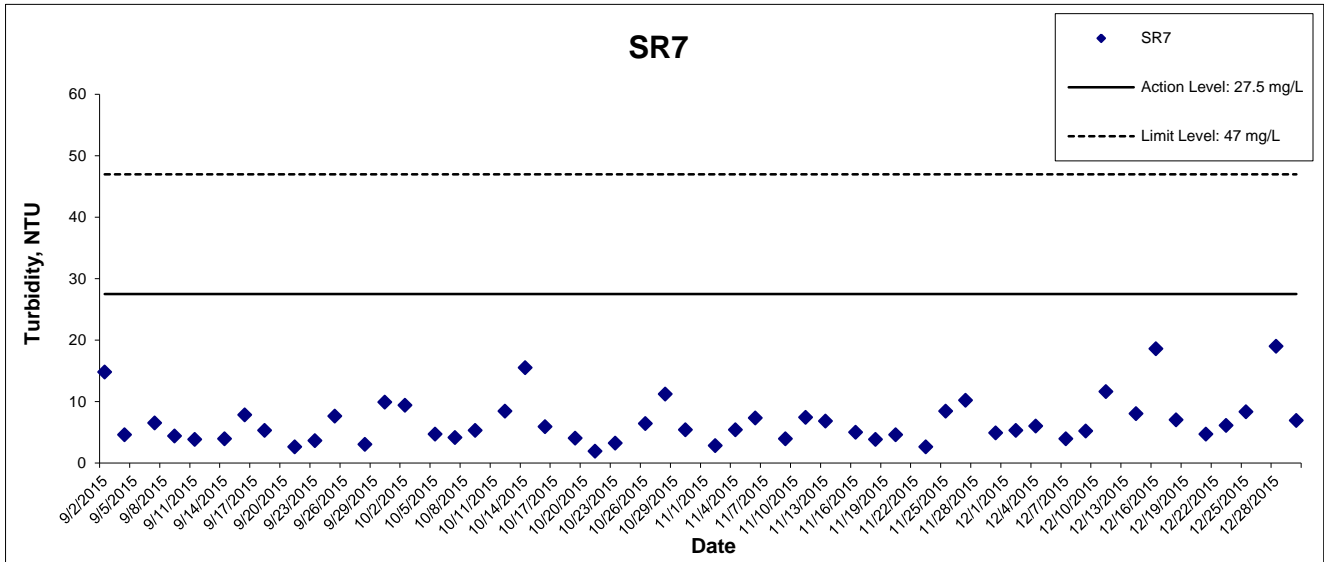




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

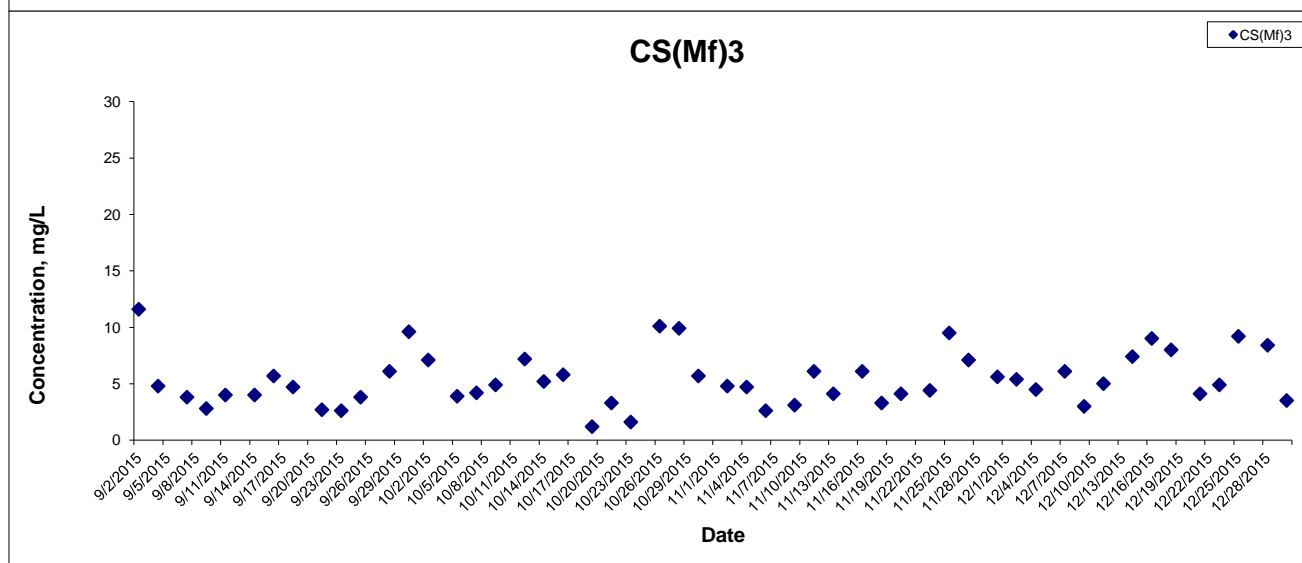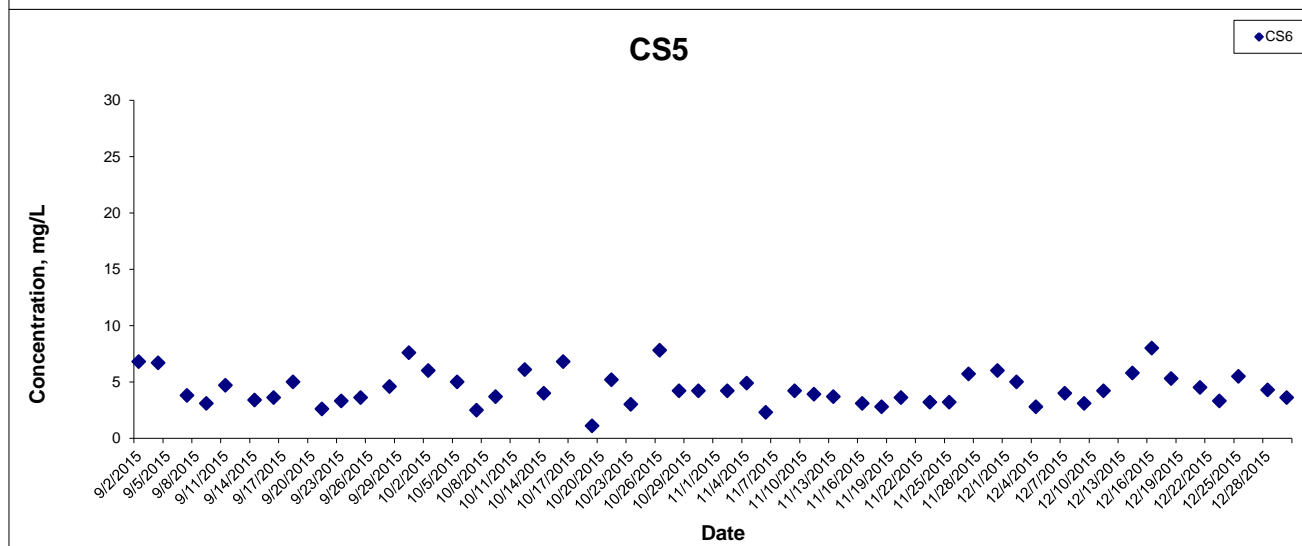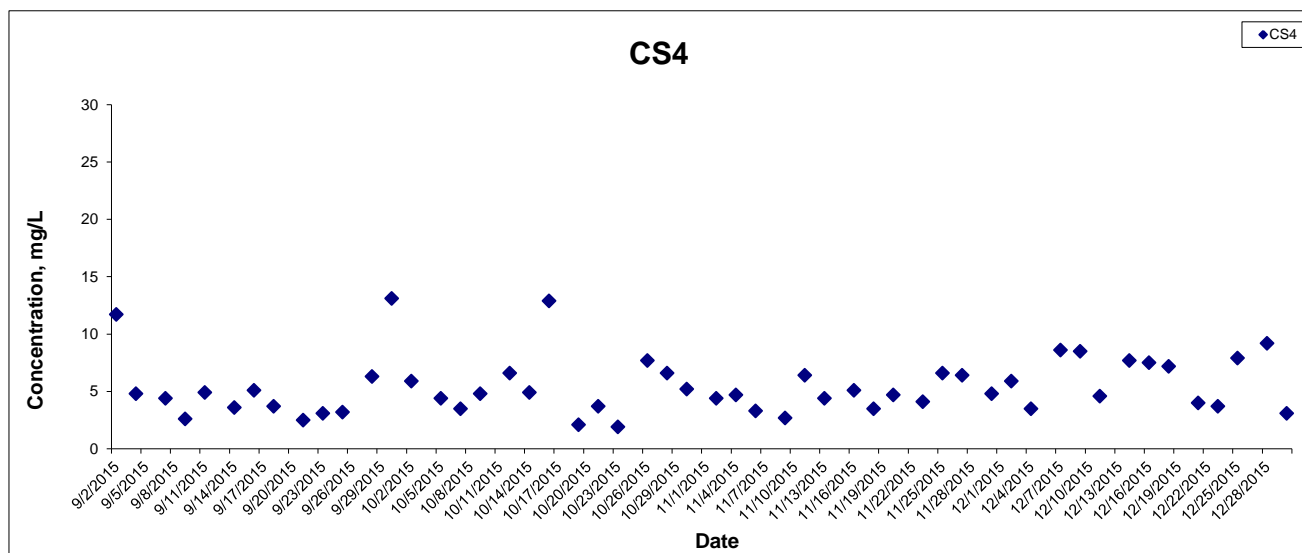

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

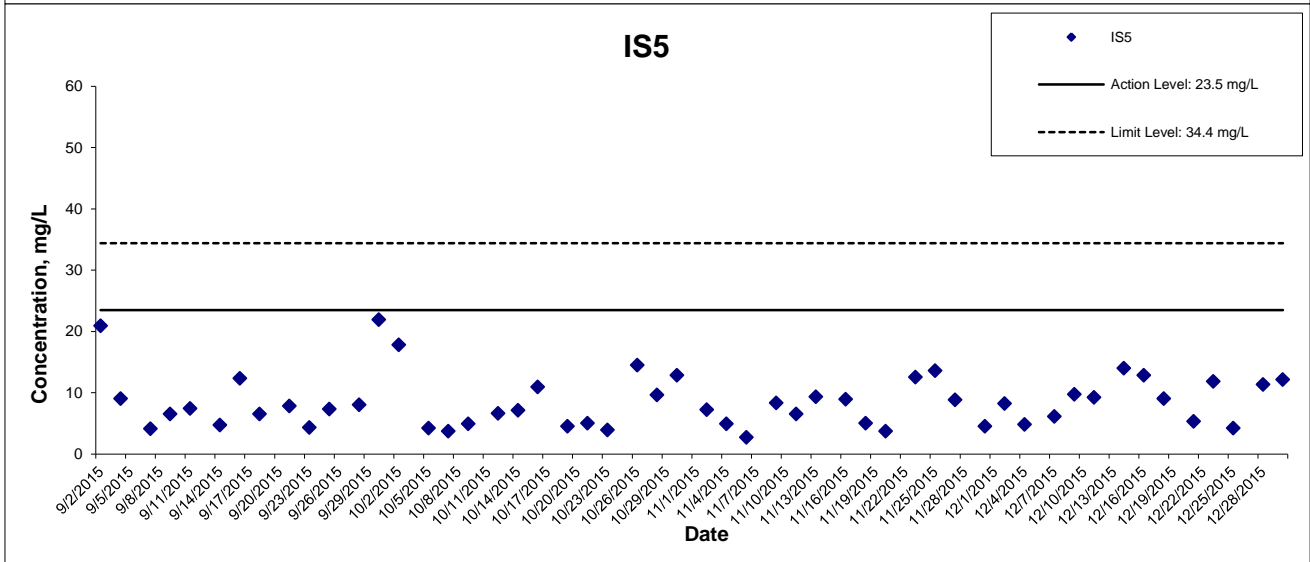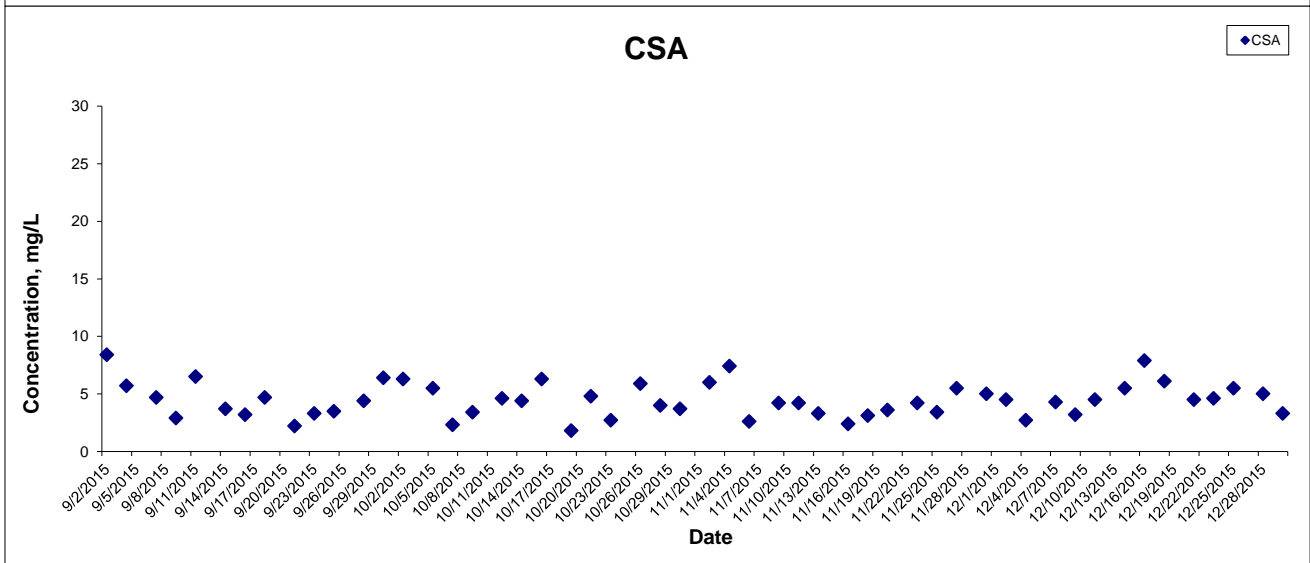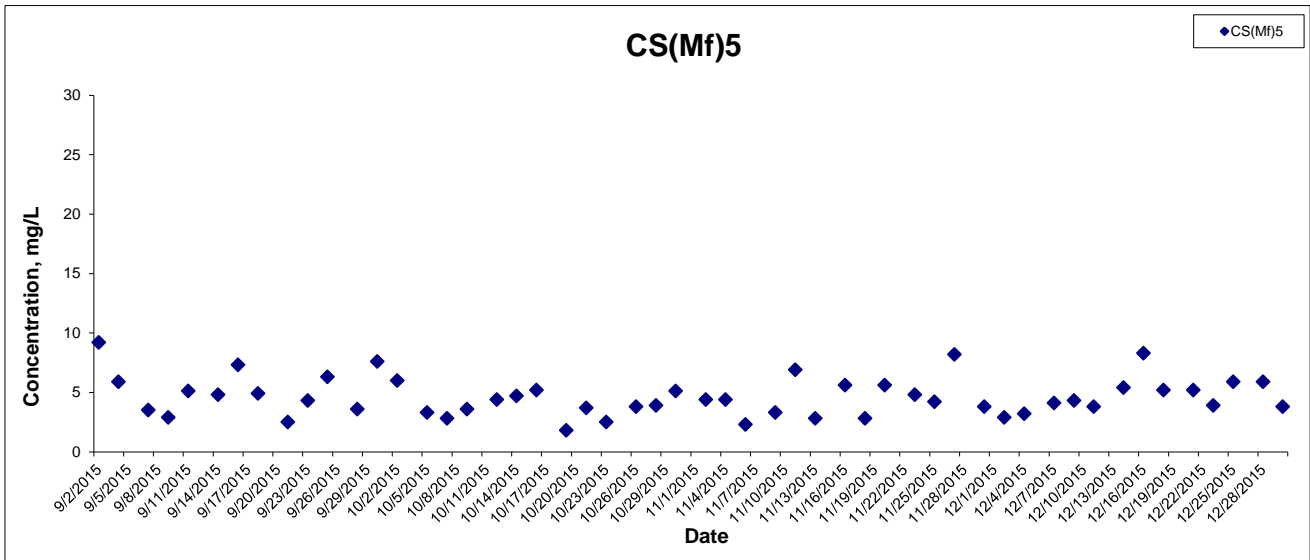




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results






Suspended Solids at Mid-Ebb Tide

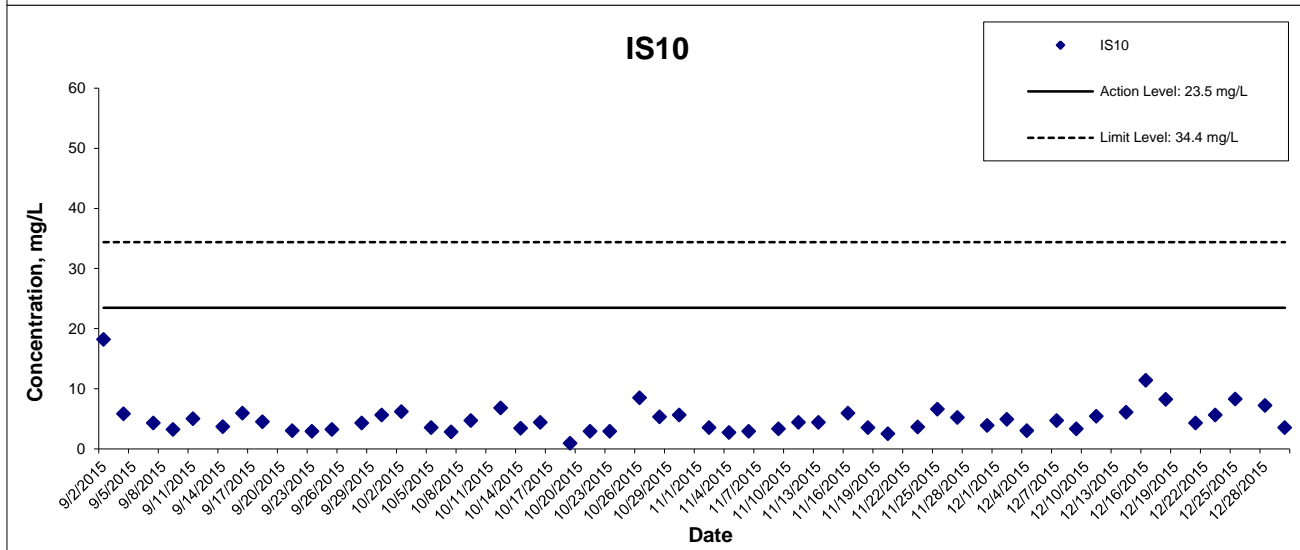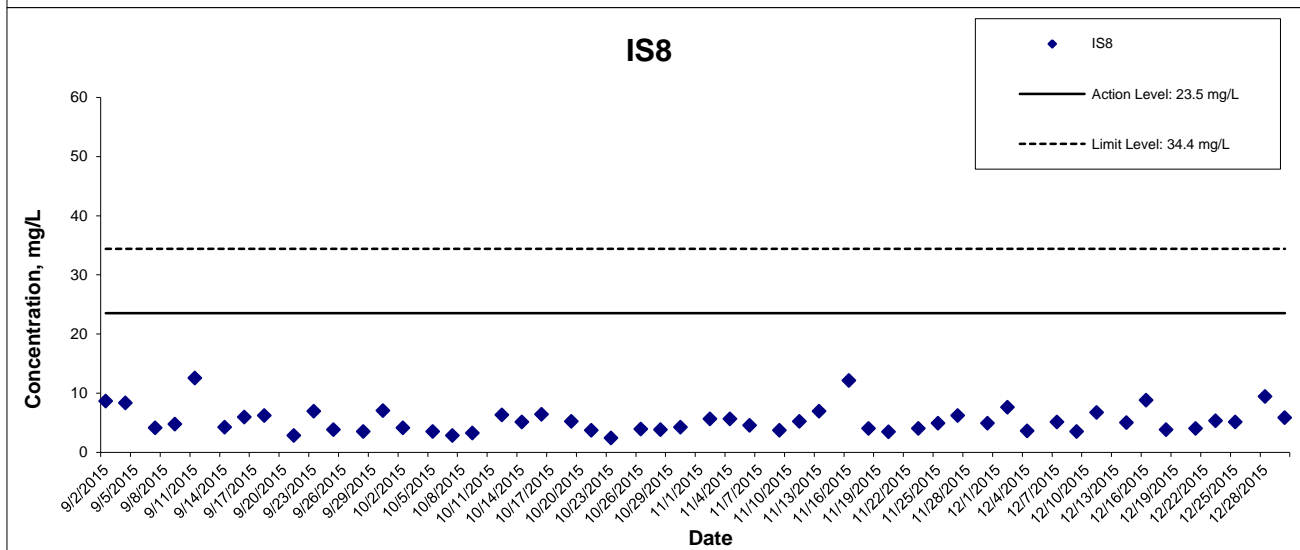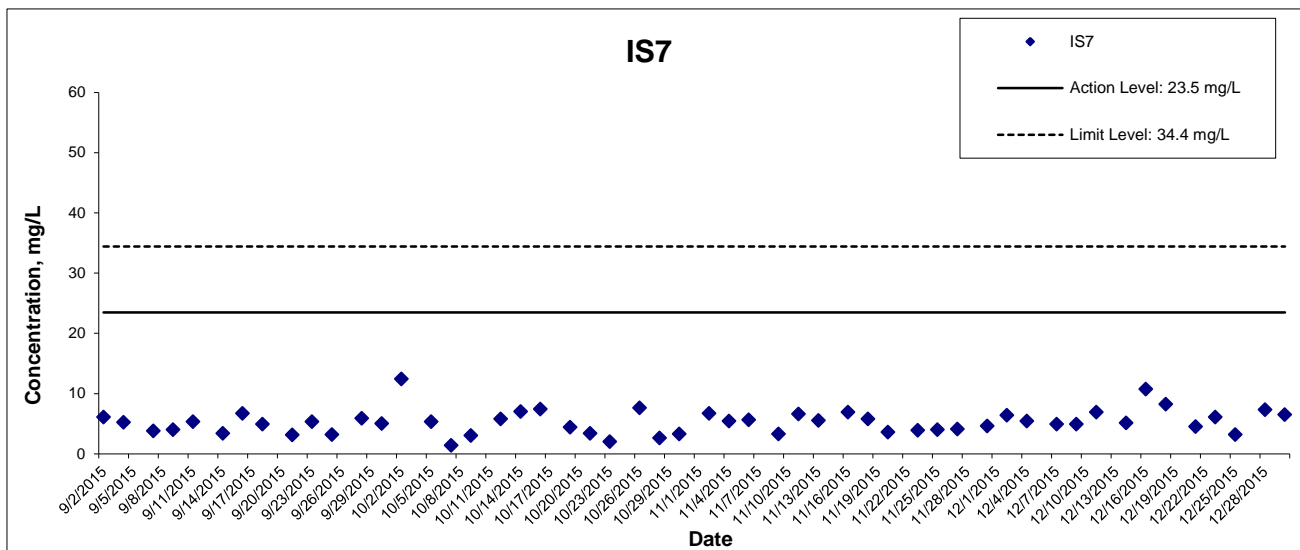




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

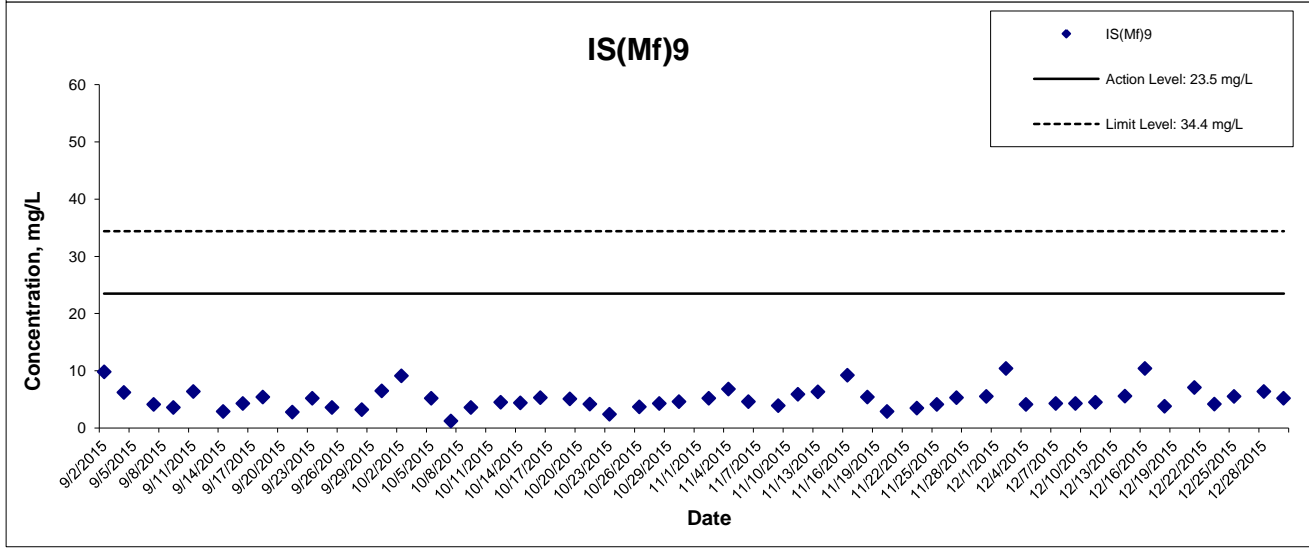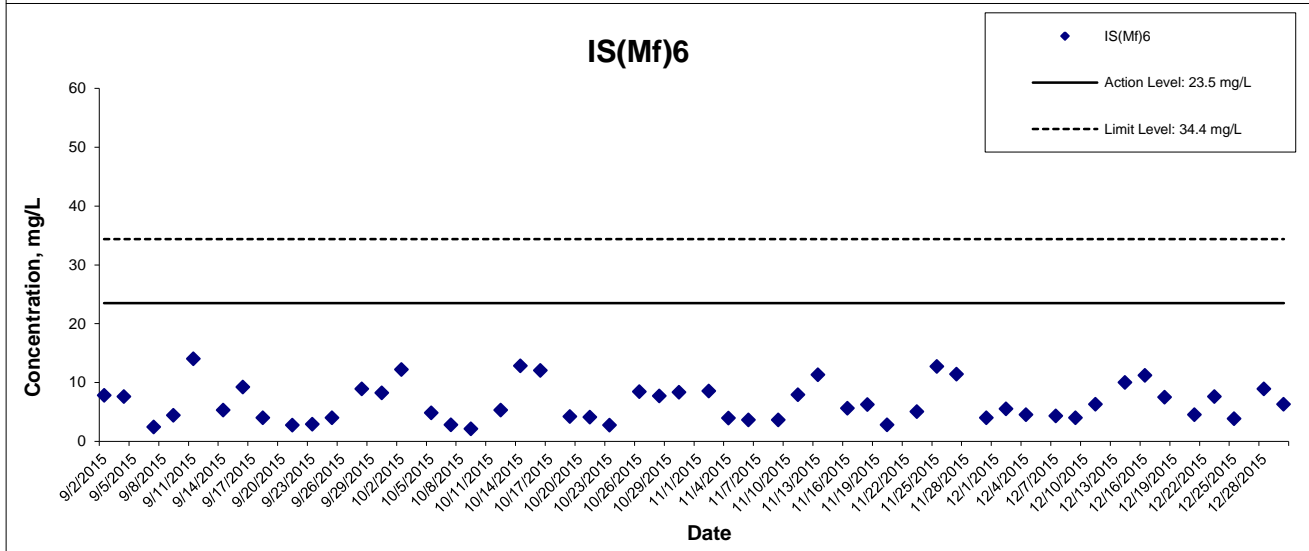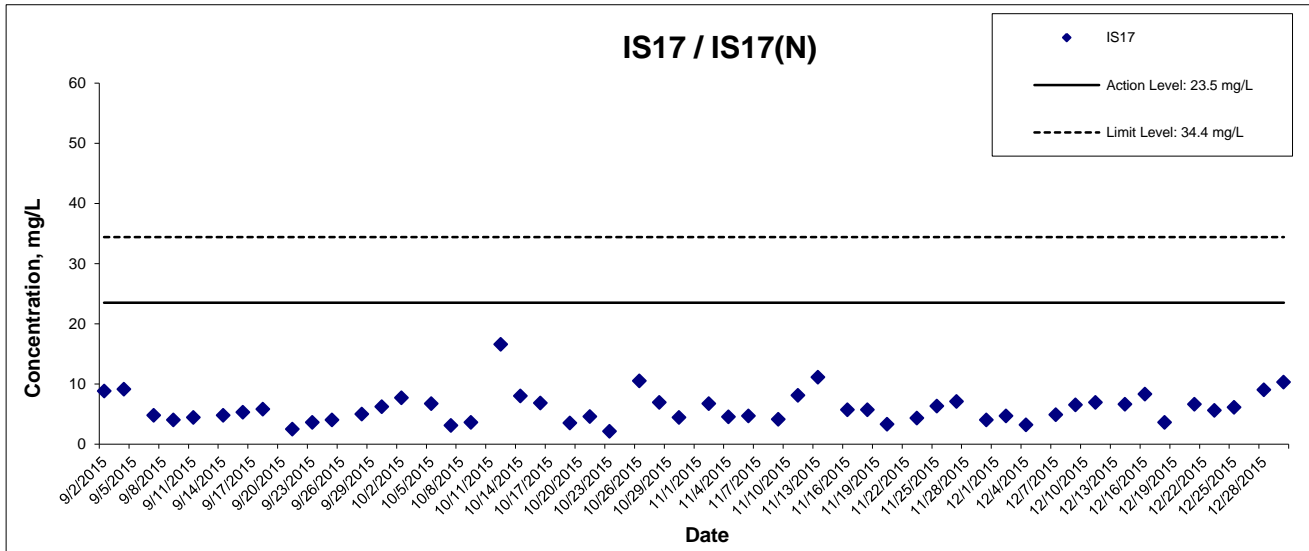




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

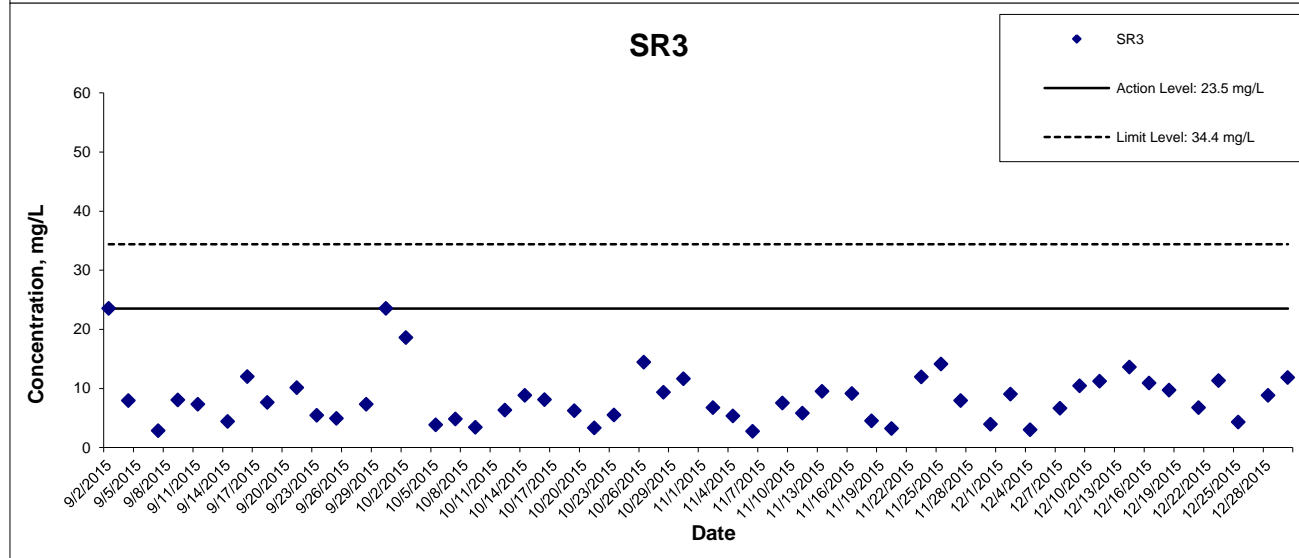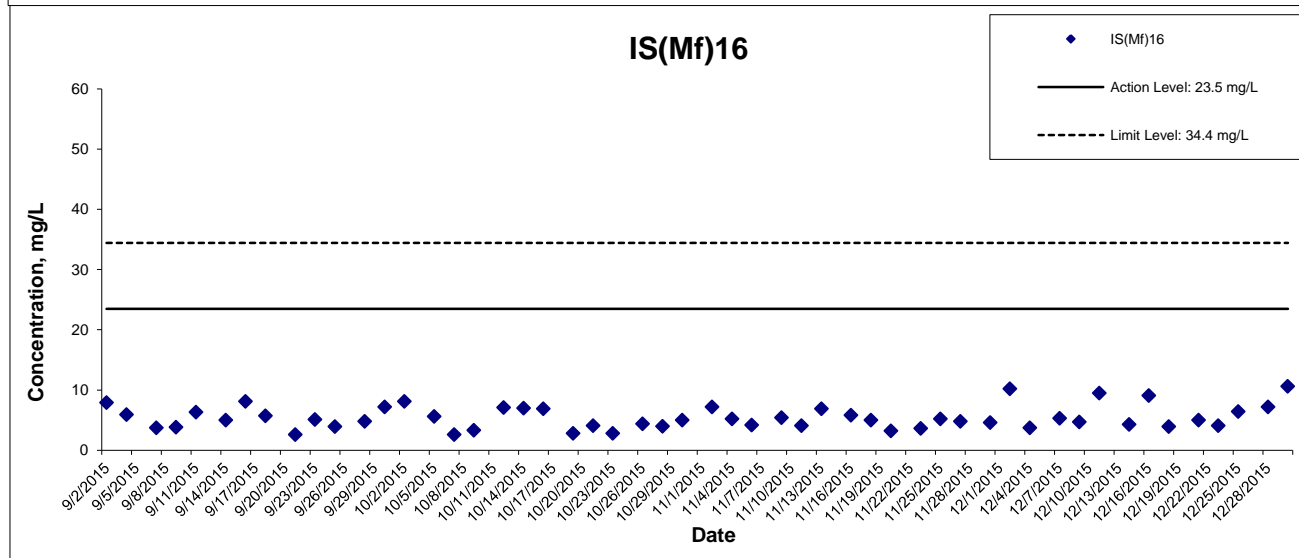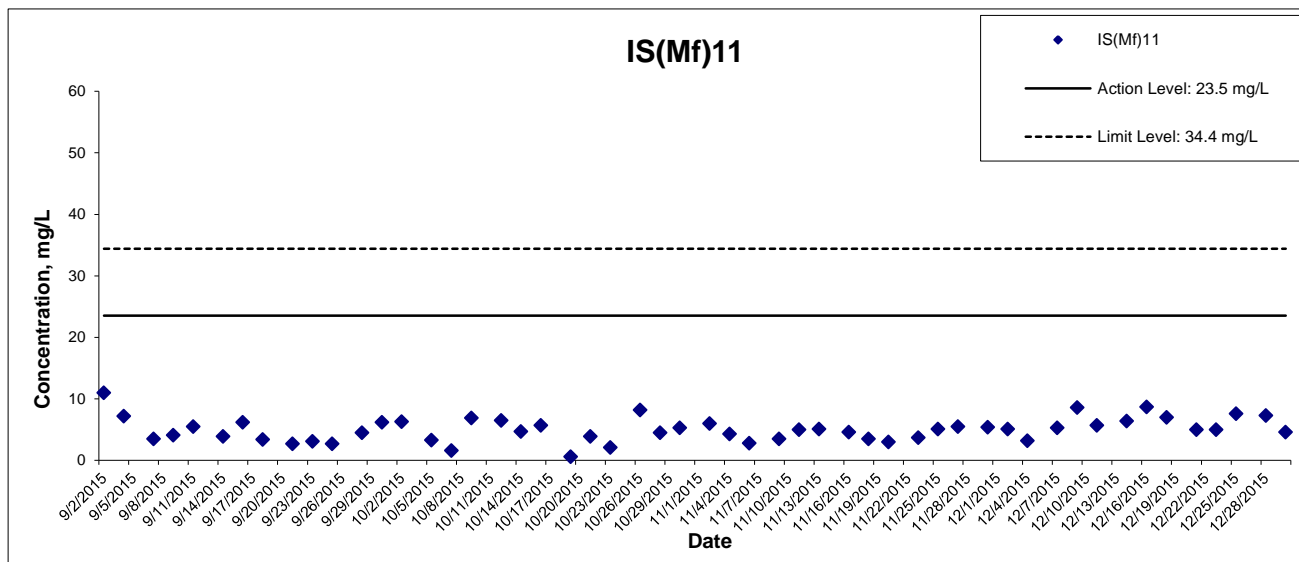




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

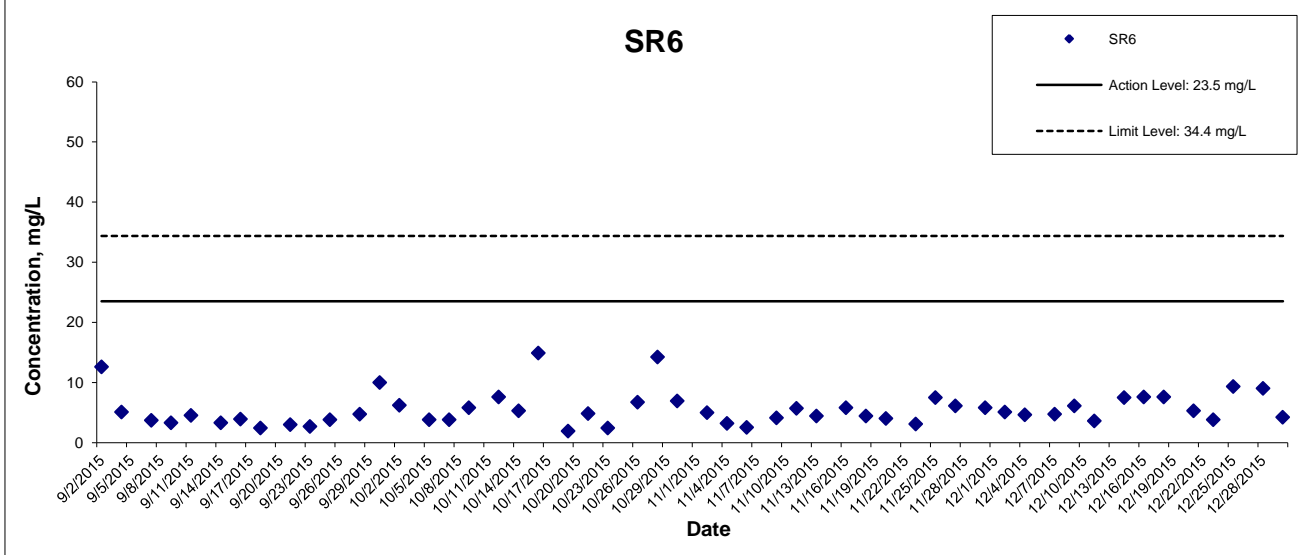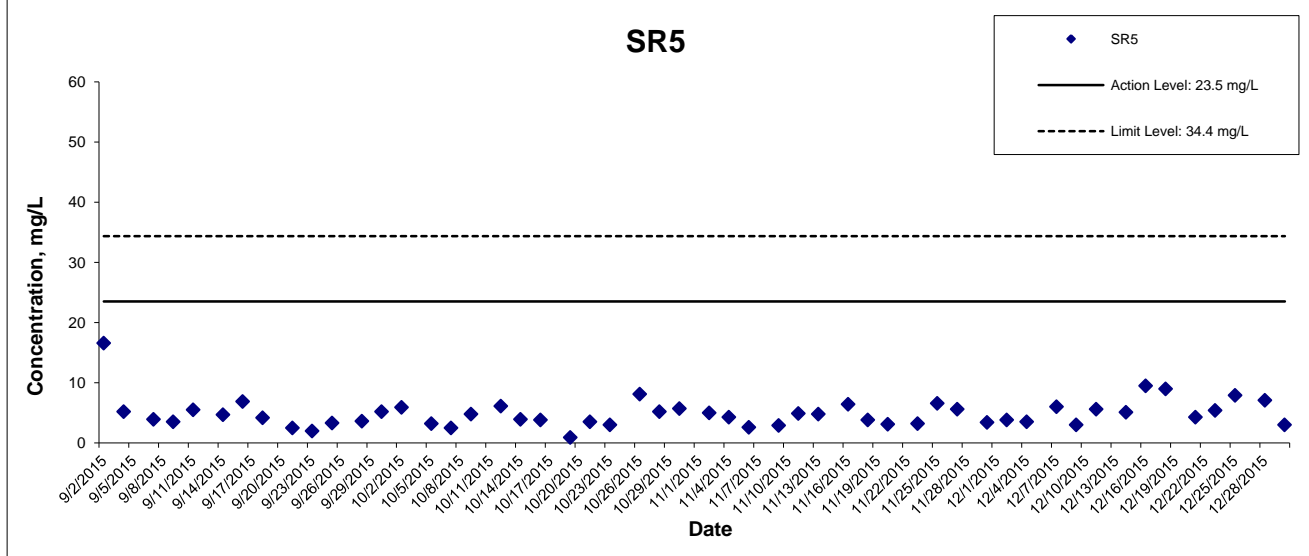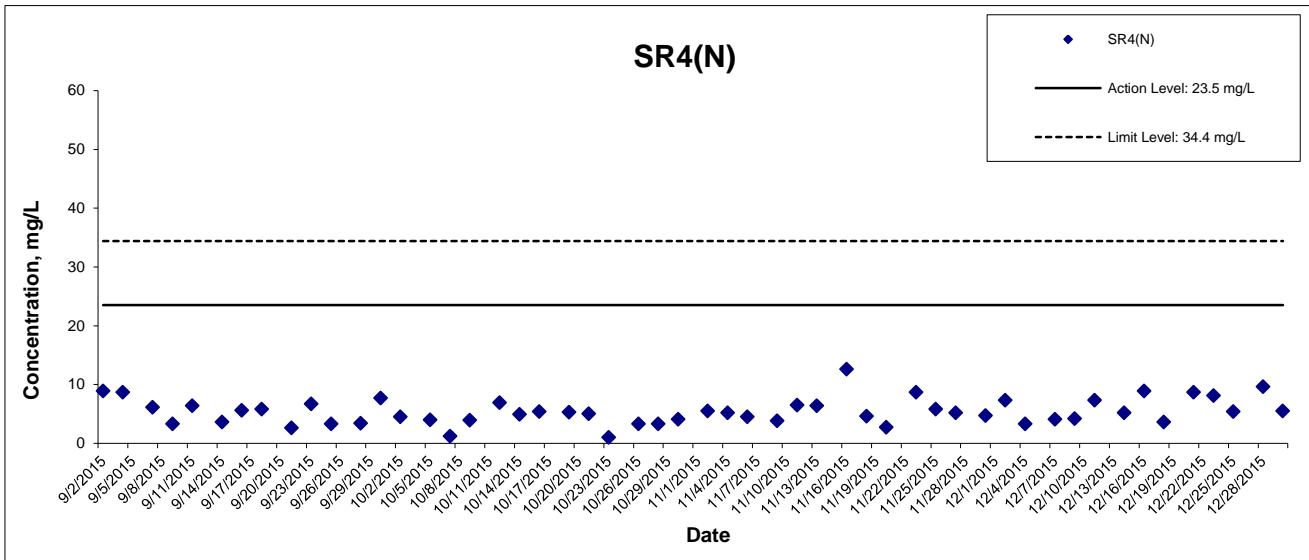




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

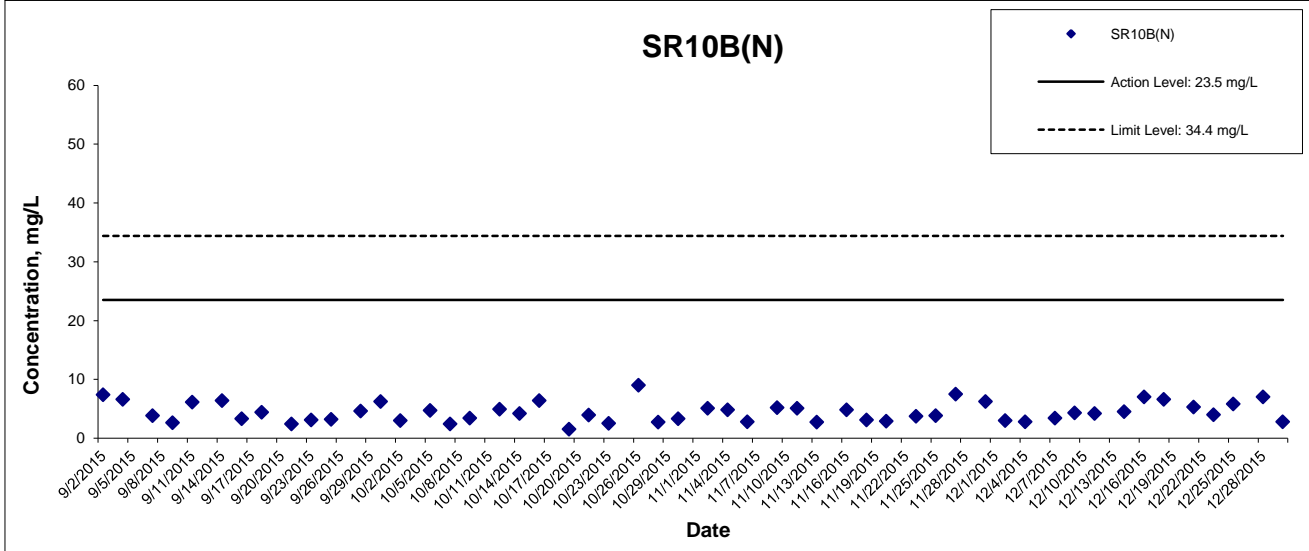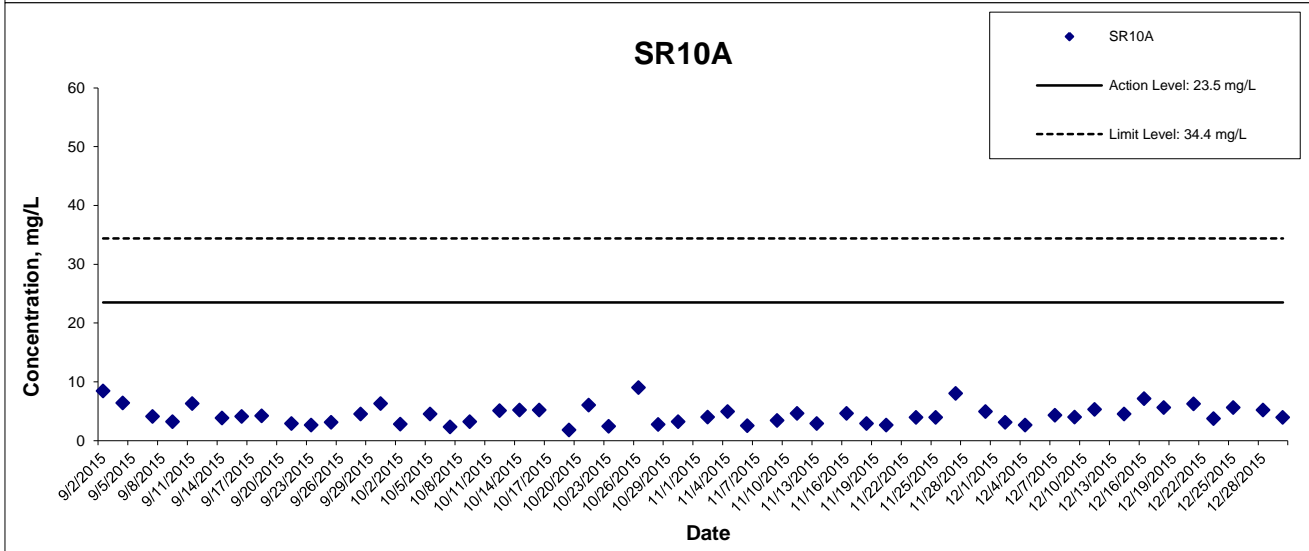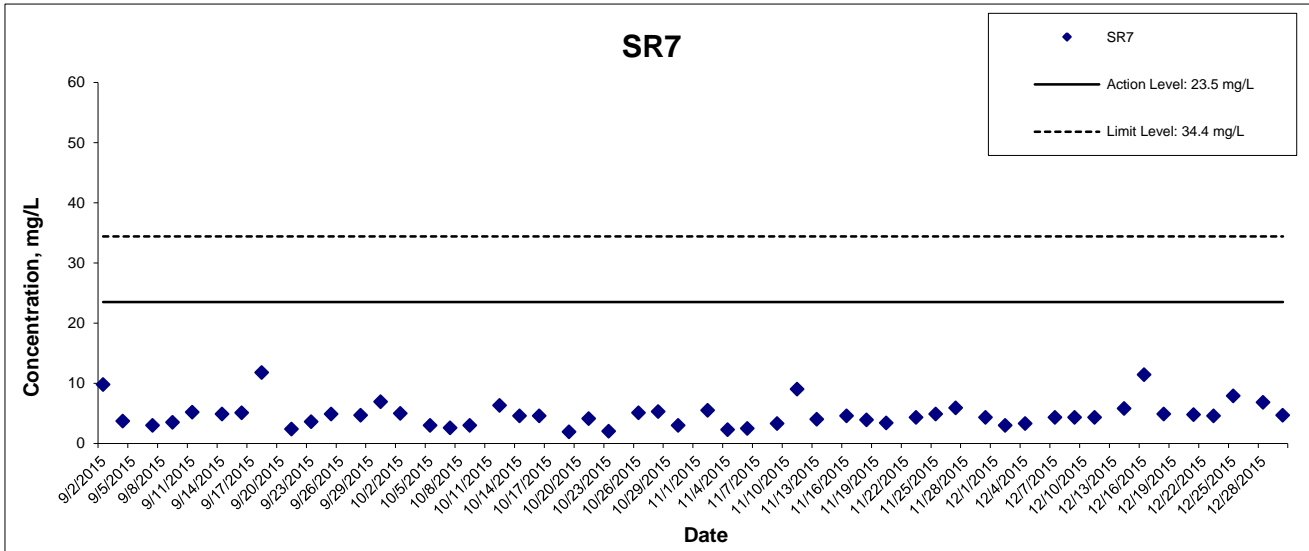

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

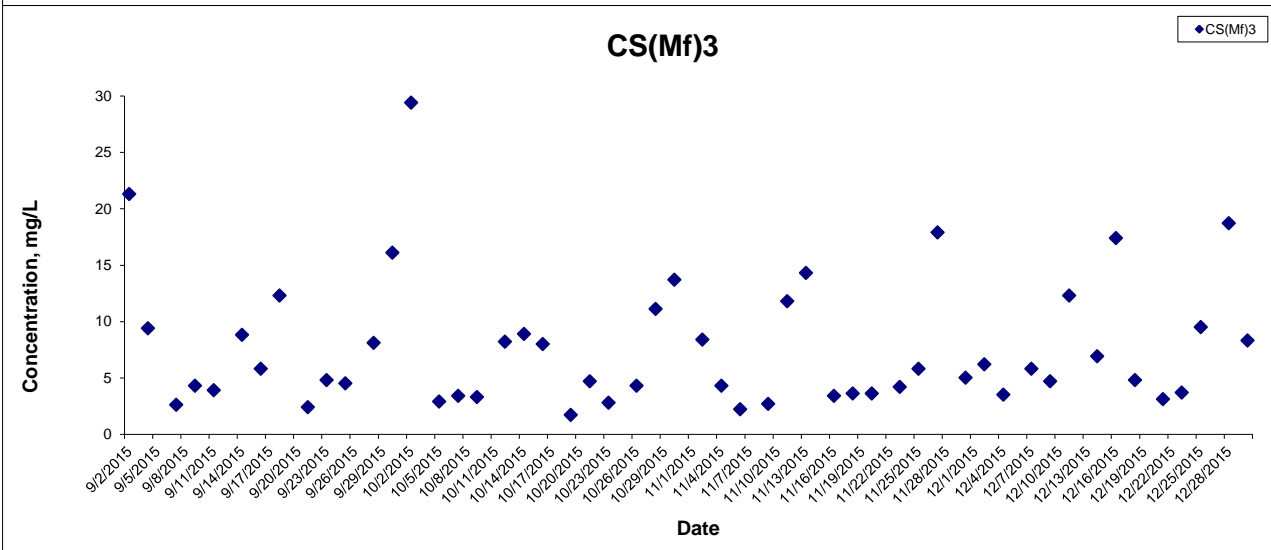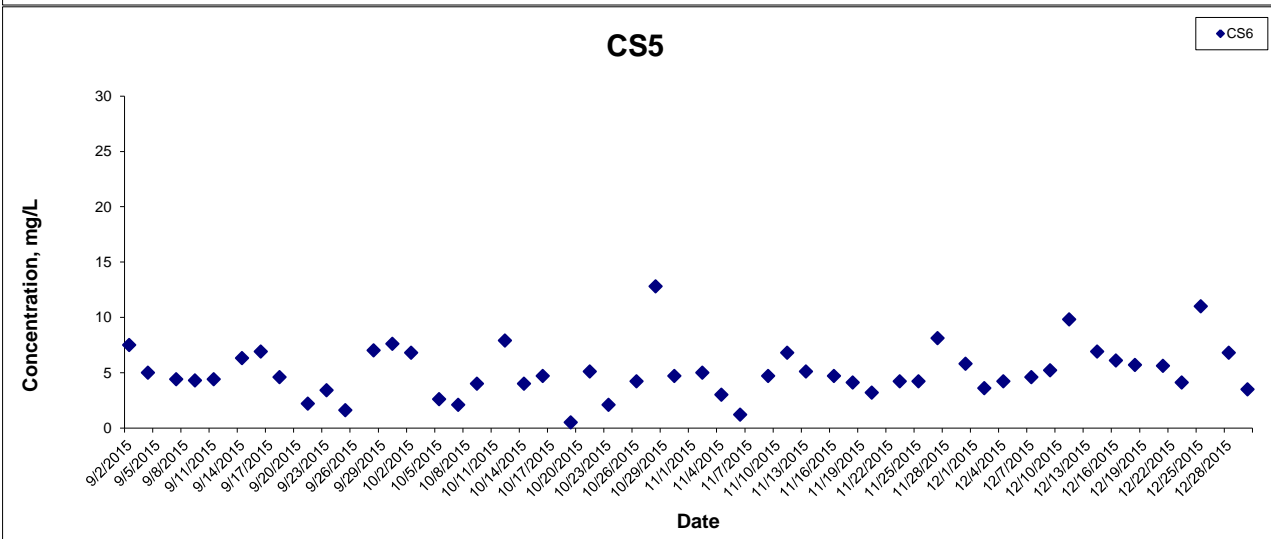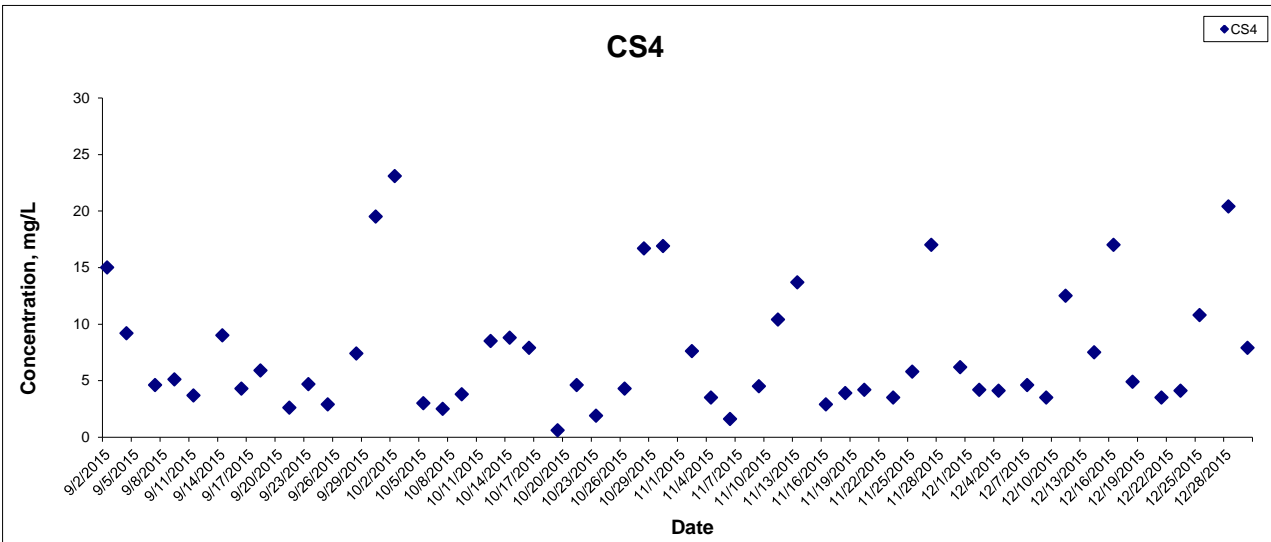

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE

HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results






Project No.: 60249820

Date: January 2016




Appendix J

Suspended Solids at Mid-Flood Tide

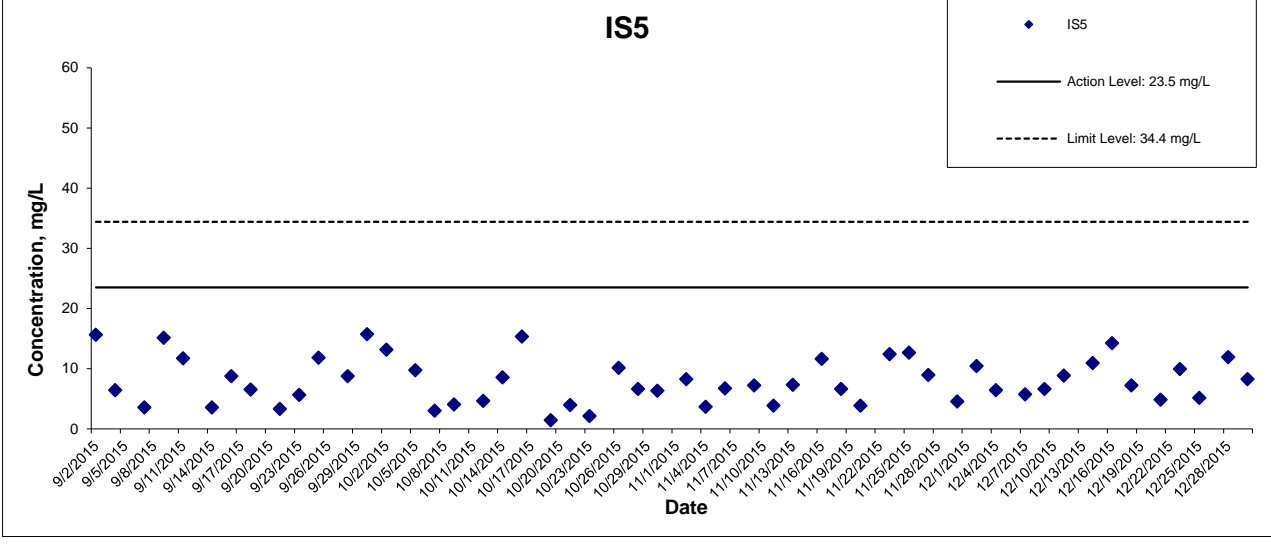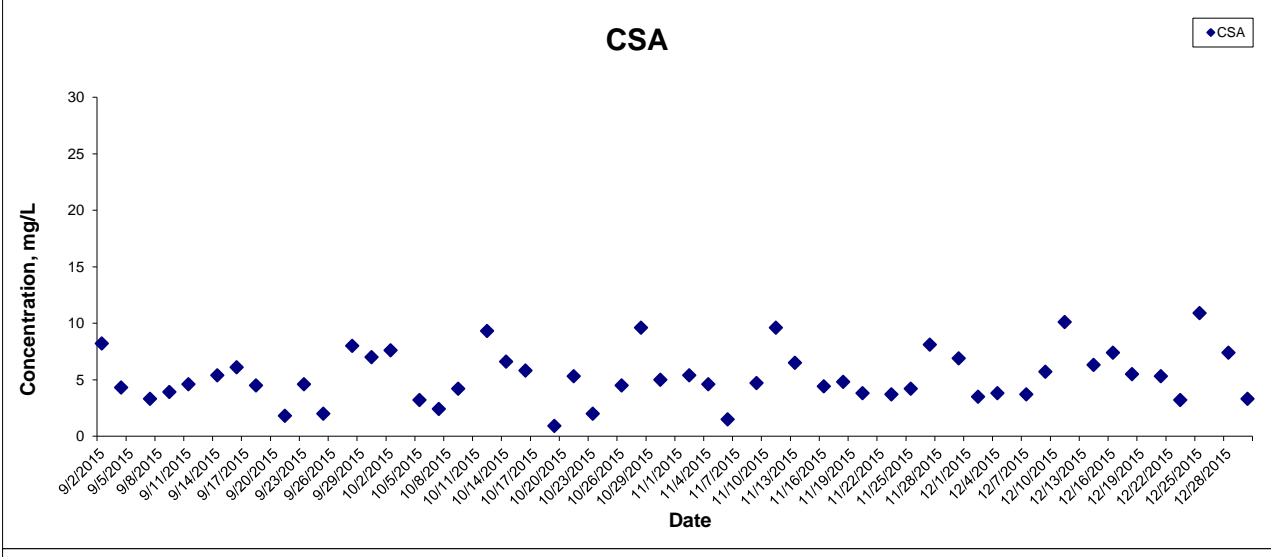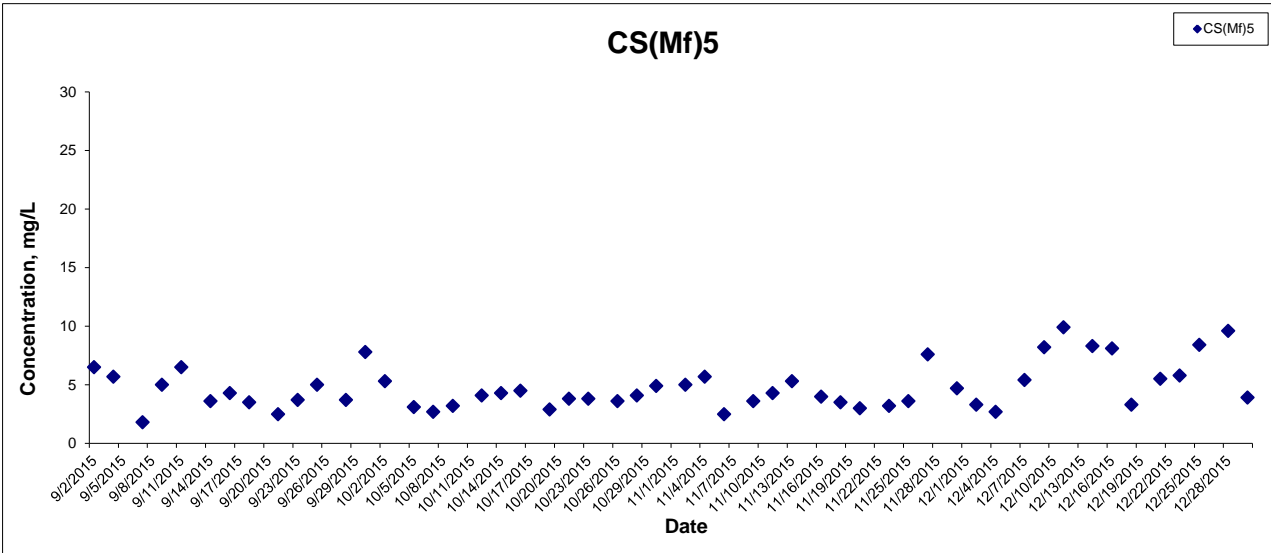




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

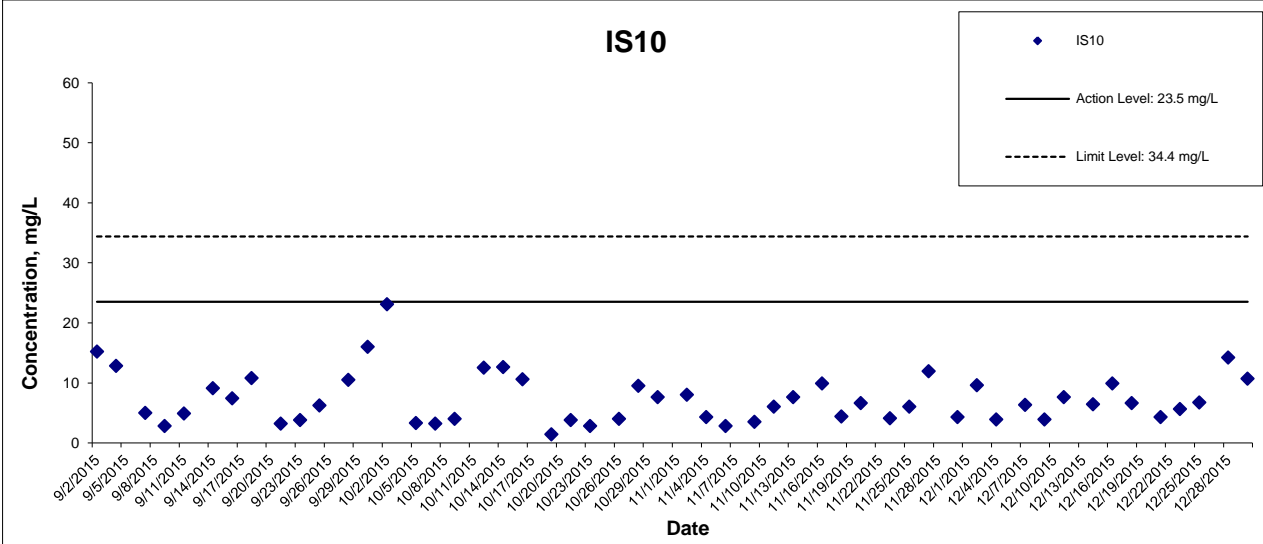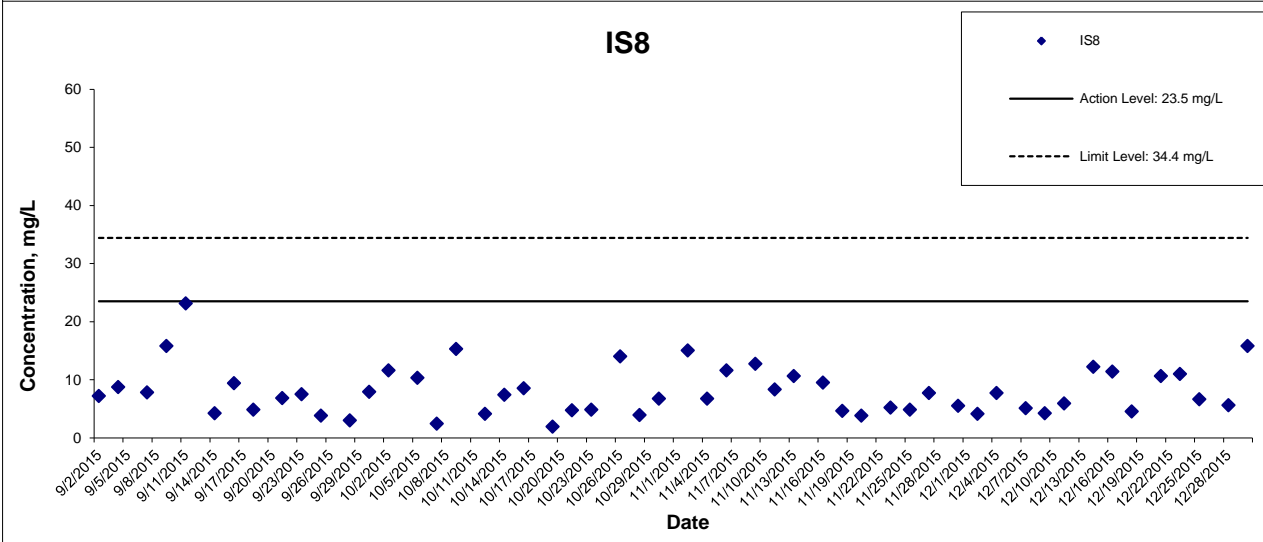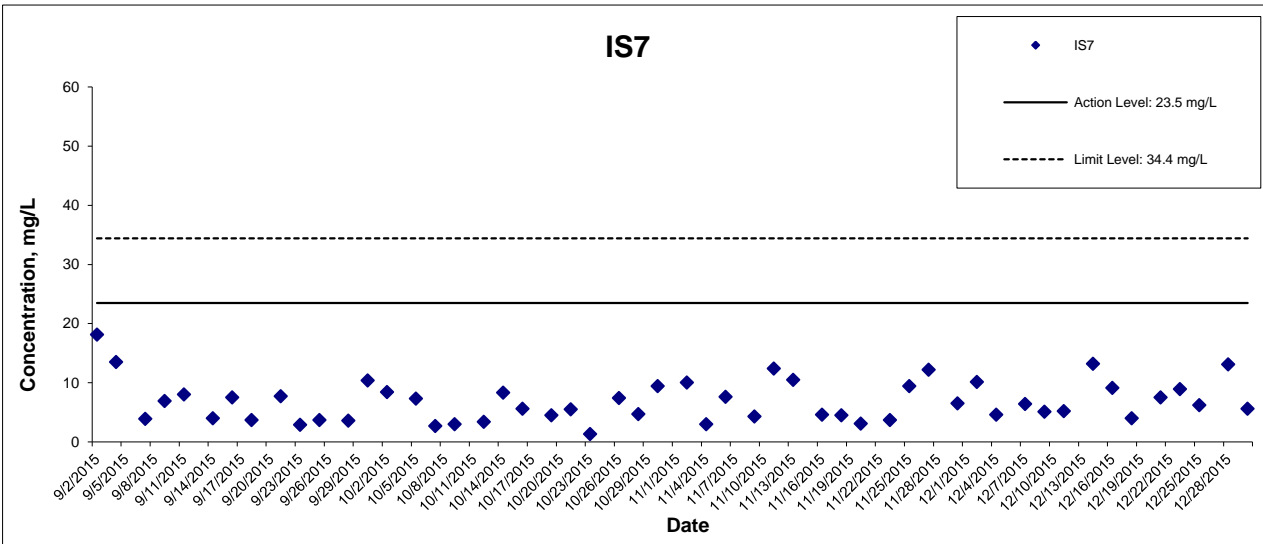

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

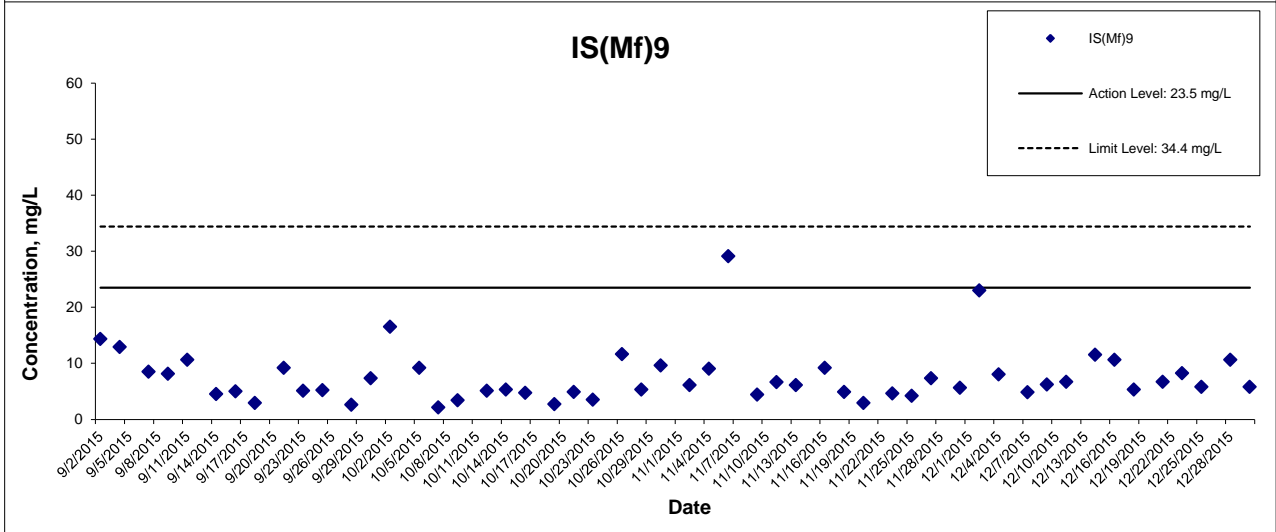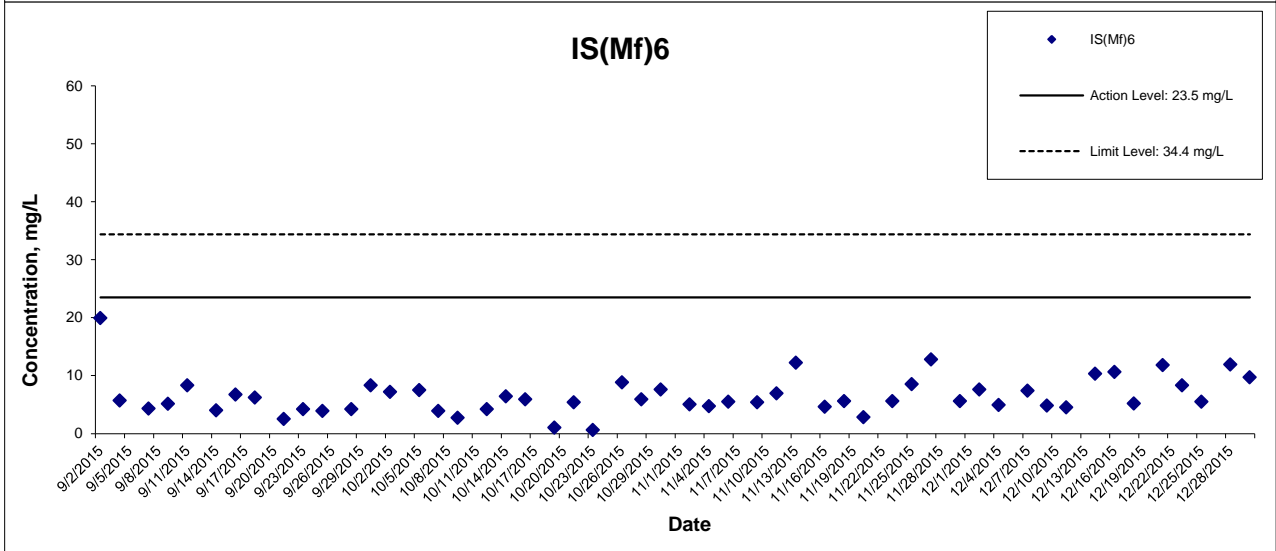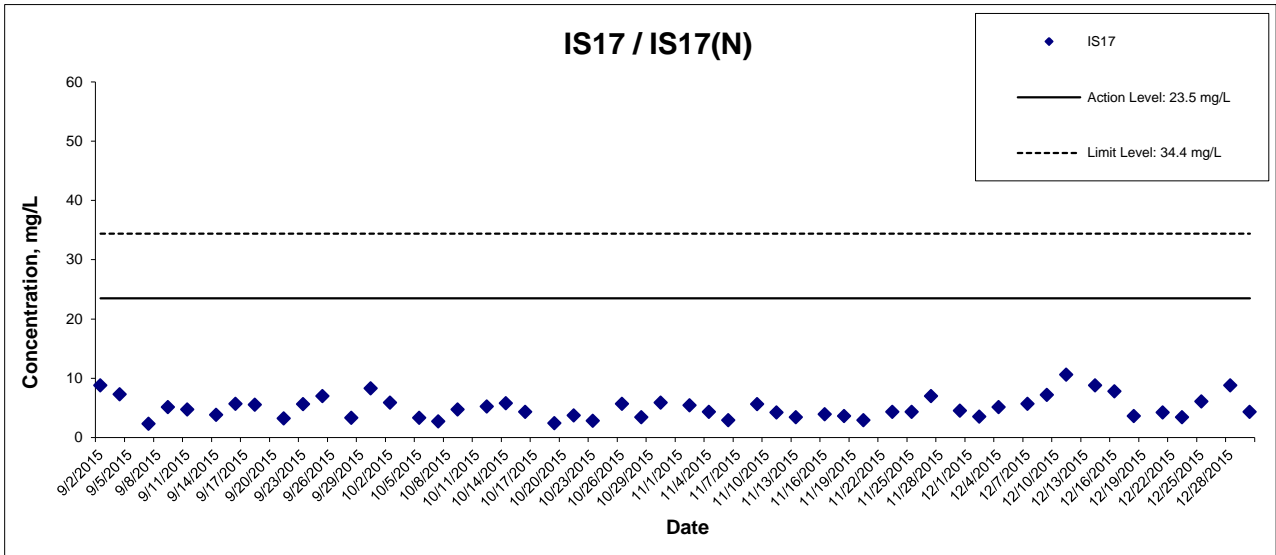

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE

HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**






Project No.: 60249820

Date: January 2016




Appendix J

Suspended Solids at Mid-Flood Tide

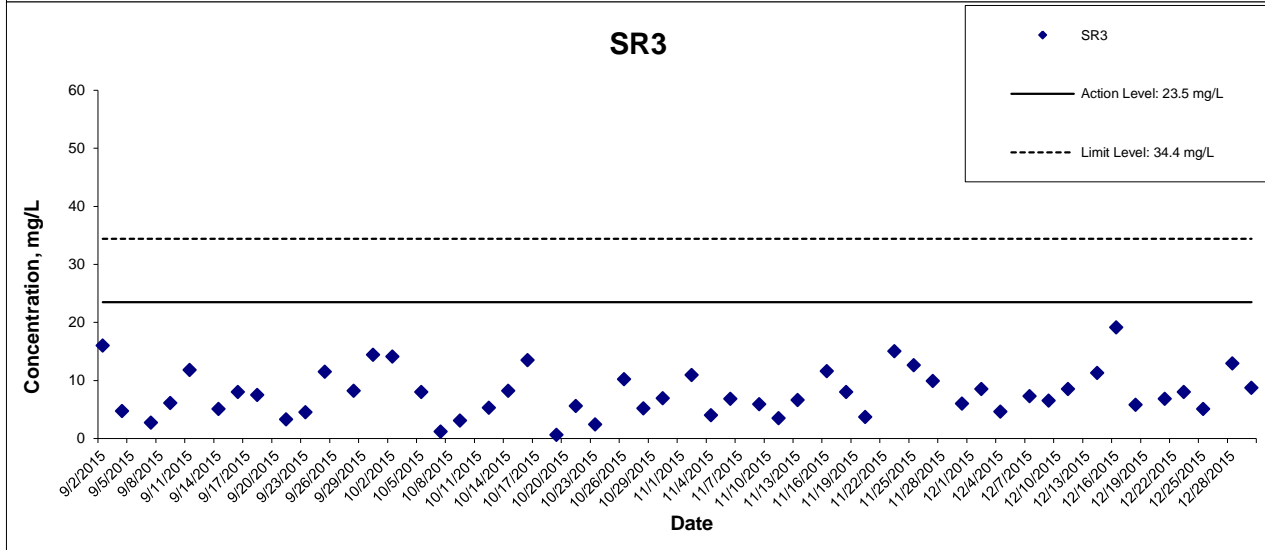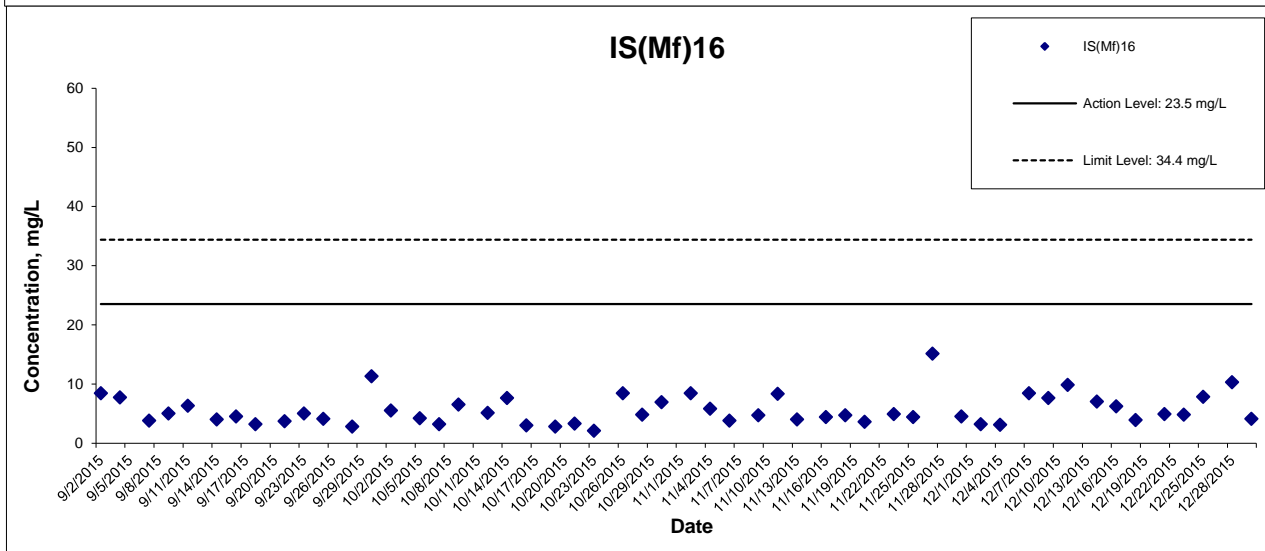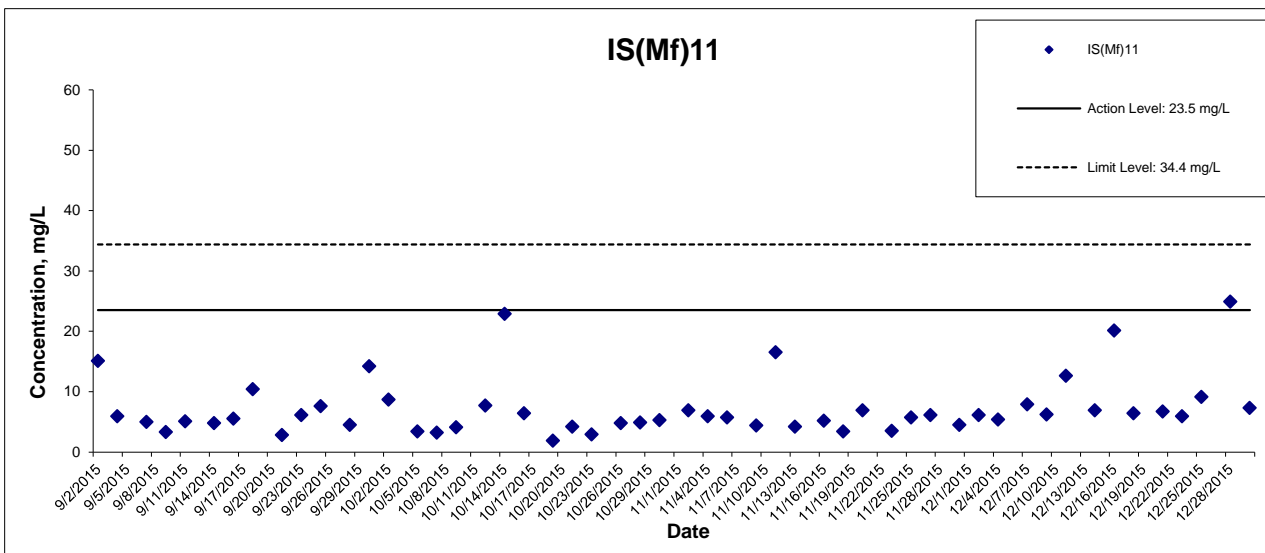




This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

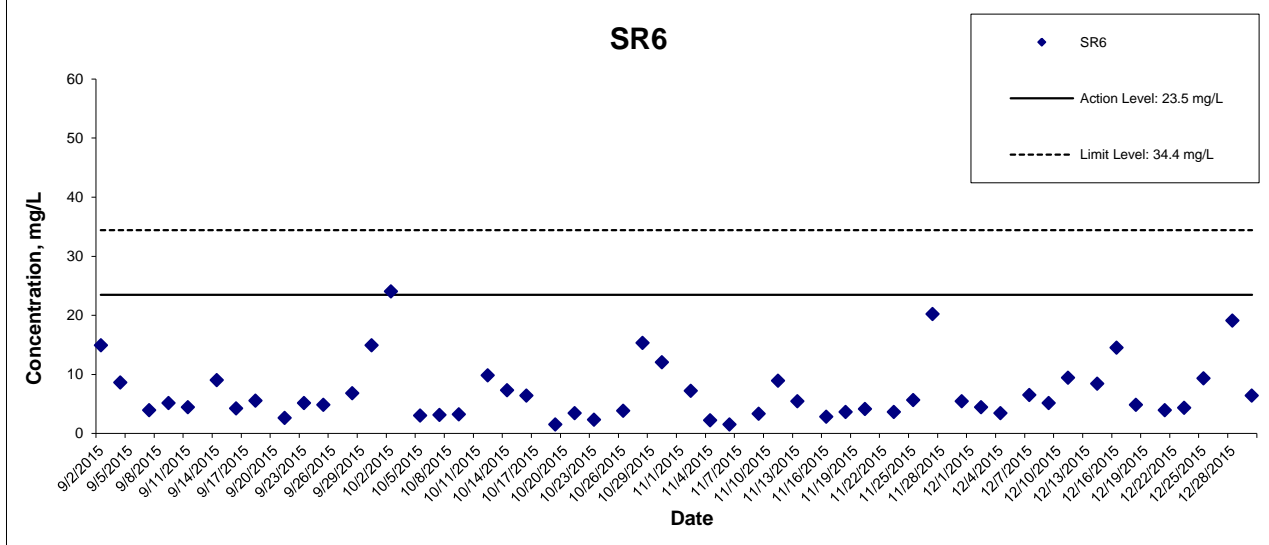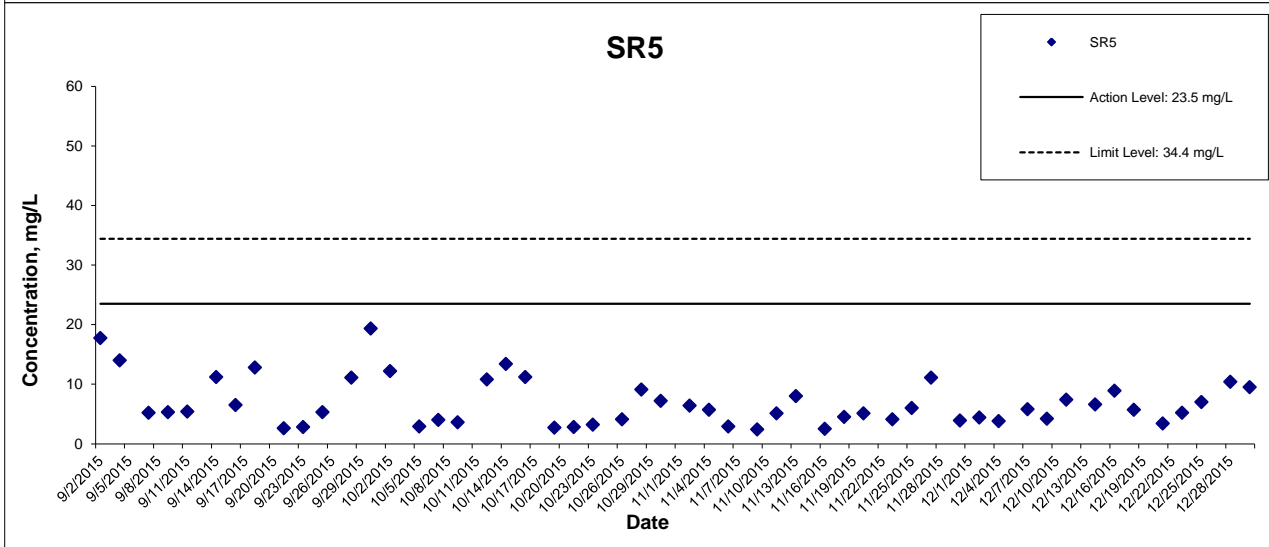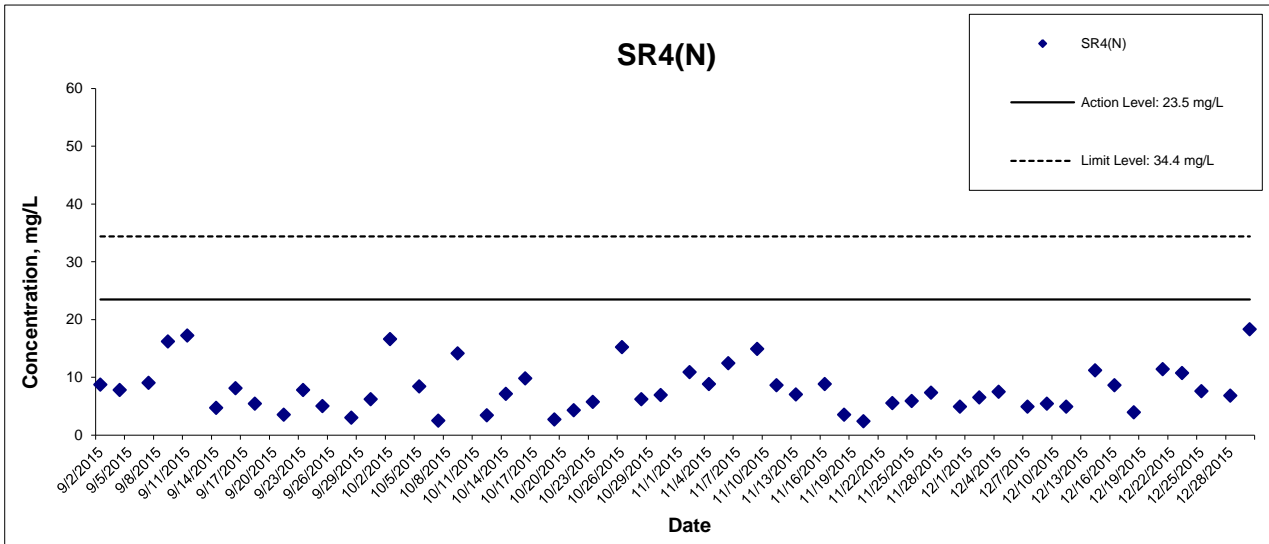

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

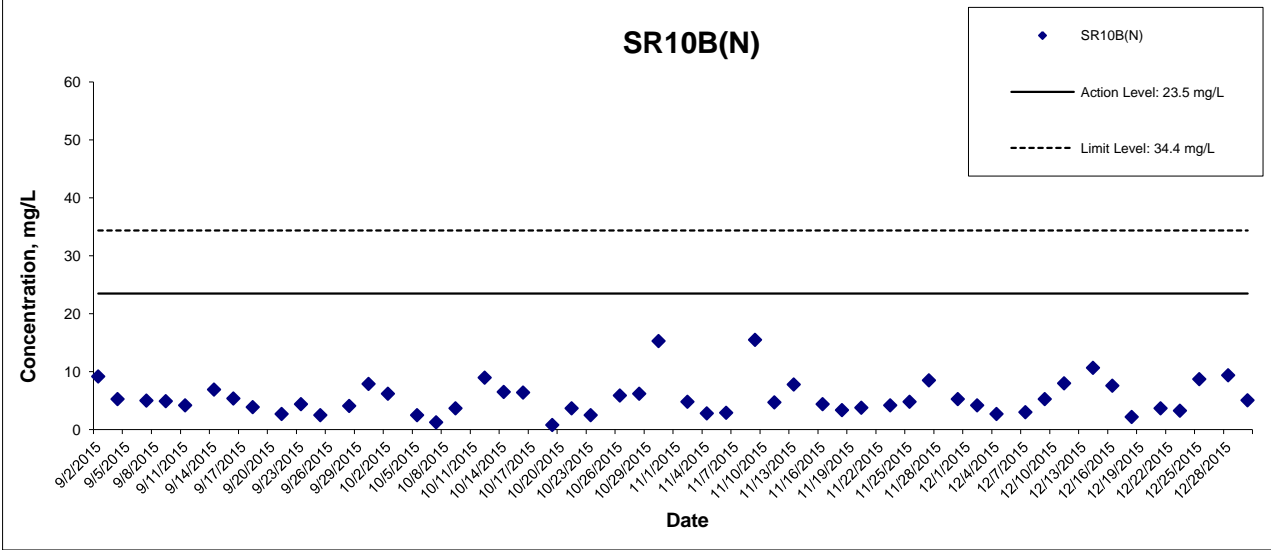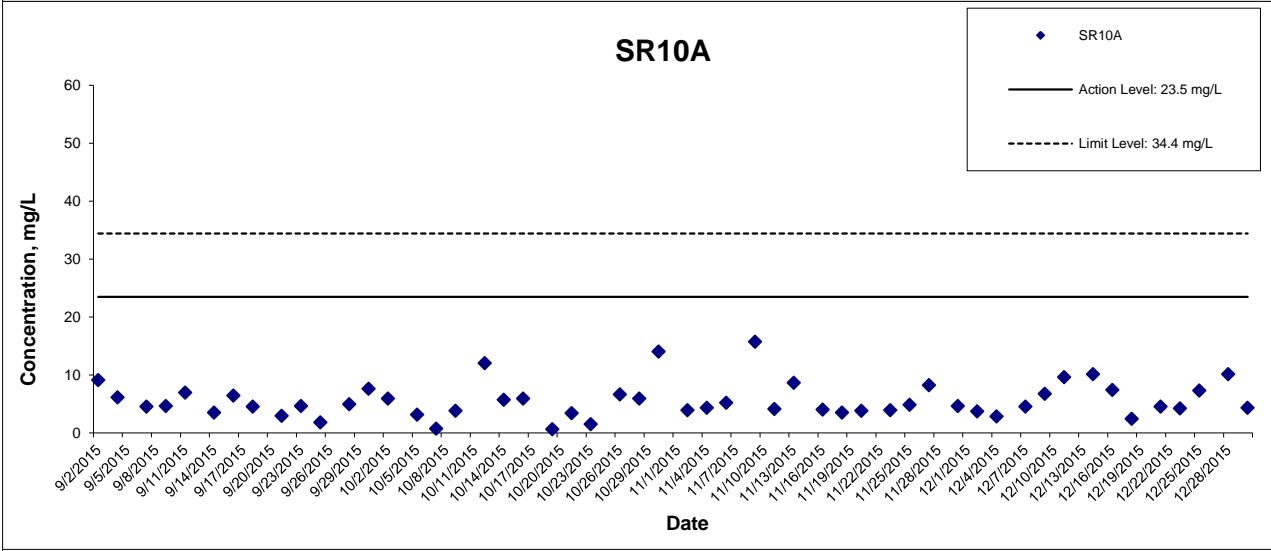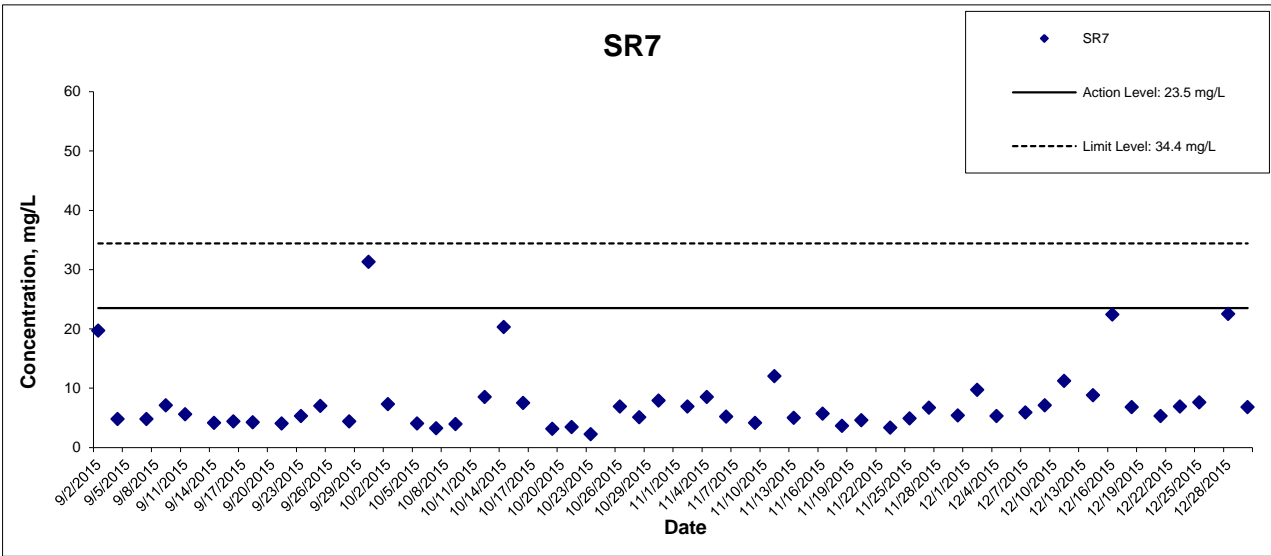

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Appendix K Impact Dolphin Monitoring Survey Sighting Summary

Table 1 Impact Dolphin Monitoring Survey Sighting Table

Project	Contract	Date	Sighting No.	Time	Group Size	Area	Beaufort	PSD	Effort	Type	Northing	Easting	Season	Boat Association
HKBCF	HY/2010/02	01-Dec-15	1178	09:48:35	3	NWL	1	17	On	Impact	815811.9	804924.9	Winter	No
HKBCF	HY/2010/02	01-Dec-15	1180	13:20:14	8	NWL	2	0	On	Impact	824192.2	806755.0	Winter	No

KEY:

Sighting Opp Opportunistic
 On On effort

PSD Perpendicular Sighting Distance NEL North East Lantau

Group Size Represents best estimate for group encountered NWL North West Lantau

Annex I

November 2015 Photo Identification Information

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 129		22/10/2015	1156	NWL
		07/09/2015	1143	NWL
		25/08/2015	1138	NWL
HZMB 128		03/01/2015	1056	NWL
HZMB 127		03/01/2015	1056	NWL
HZMB 126		23/02/2015	1068	NWL
		03/01/2015	1054	NWL
HZMB 125		13/10/2014	1019	NWL
HZMB 124		22/09/2014	1005	NWL
HZMB 123		25/08/2014	998	NWL
HZMB 122		22/10/2015	1156	NWL
		04/08/2014	989	NWL
HZMB 121		14/07/2014	968	NWL
HZMB 120		31/05/2014	951	NWL
HZMB 119		19/04/2014	940	NWL
HZMB 118		06/01/2014	890	NWL
HZMB 117		17/06/2014	964	NWL
		06/01/2014	888	NWL
HZMB 116		25/08/2014	999	NWL
HZMB 115		14/07/2014	972	NWL
		14/07/2014	971	NWL
		26/12/2013	879	NWL
		26/12/2013	879	NWL
HZMB 114		05/11/2015	1162	NWL
		24/10/2013	827	NWL
HZMB 113		24/10/2013	827	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 112		15/10/2013	815	NWL
HZMB 111		15/10/2013	815	NWL
HZMB 110		15/10/2013	812	NWL
HZMB 108		11/06/2015	1118	NWL
		30/08/2013	780	NEL
HZMB 107		28/07/2015	1126	NWL
		13/10/2014	1019	NWL
		31/05/2014	951	NWL
		21/08/2013	770	NWL
HZMB 106		21/08/2013	769	NWL
HZMB 105		31/05/2014	951	NWL
		08/07/2013	711	NWL
HZMB 104		08/07/2013	711	NWL
HZMB 103		08/07/2013	711	NWL
HZMB 102		08/07/2013	706	NWL
HZMB 101		08/07/2013	706	NWL
HZMB 100		08/07/2013	706	NWL
HZMB 099		13/06/2013	681	NWL
		13/06/2013	680	NWL
HZMB 098	NL104	23/02/2015	1077	NWL
		18/12/2014	1044	NWL
		04/08/2014	992	NWL
		06/01/2014	888	NWL
		02/11/2013	849	NWL
		02/11/2013	845	NWL
		24/10/2013	831	NWL
		08/07/2013	711	NWL
		24/05/2013	659	NWL
		07/11/2011	Baseline	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		05/11/2011	Baseline	NWL
		05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		28/10/2011	Baseline	NWL
		23/09/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
HZMB 097		09/05/2013	647	NWL
HZMB 096		01/04/2013	621	NWL
HZMB 095		30/08/2013	780	NEL
		25/06/2013	697	NWL
		13/06/2013	682	NWL
		01/04/2013	621	NWL
HZMB 094		13/10/2014	1019	NWL
		31/05/2014	954	NWL
		17/02/2014	910	NWL
		26/06/2013	703	NWL
		25/06/2013	698	NWL
		18/03/2013	601	NWL
HZMB 093		24/05/2013	657	NWL
		21/02/2013	587	NWL
HZMB 092		20/04/2015	1097	NWL
		21/02/2013	589	NWL
		15/02/2013	581	NWL
HZMB 091		15/02/2013	579	NWL
HZMB 090		25/06/2013	697	NWL
		13/06/2013	682	NWL
		15/02/2013	579	NWL
HZMB 089		15/02/2013	579	NWL
HZMB 088		15/02/2013	579	NWL
HZMB 087		15/02/2013	579	NWL
HZMB 086	NL242	19/03/2015	1086	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		09/05/2013	642	NWL
		15/02/2013	579	NWL
		10/10/2011	Baseline	NWL
HZMB 085		13/10/2014	1019	NWL
		31/05/2014	954	NWL
HZMB 084		26/06/2013	703	NWL
		15/02/2013	579	NWL
		14/02/2013	575	NWL
HZMB 083	NL136	11/05/2015	1104	NWL
		19/12/2013	863	NWL
		28/03/2013	607	NWL
		15/02/2013	579	NWL
		28/01/2013	568	NWL
		28/01/2013	564	NWL
		19/04/2012	267	NWL
		28/10/2011	Baseline	NWL
		28/10/2011	Baseline	NWL
		10/10/2011	Baseline	NEL
		06/09/2011	Baseline	NWL
HZMB 082		20/10/2014	1024	NWL
		21/02/2013	587	NWL
		15/02/2013	579	NWL
		28/01/2013	563	NWL
HZMB 081		28/01/2013	559	NWL
		28/01/2013	557	NWL
HZMB 080		28/01/2013	556	NWL
HZMB 079		28/01/2013	556	NWL
HZMB 078		15/02/2013	579	NWL
		08/01/2013	552	NWL
HZMB 077		26/12/2013	878	NWL
		08/07/2013	706	NWL
		11/12/2012	541	NWL
HZMB 076		08/07/2013	706	NWL
		11/12/2012	541	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 075		06/12/2012	525	NEL
HZMB 074		09/05/2013	647	NWL
		01/04/2013	623	NWL
		01/04/2013	621	NWL
		21/02/2013	594	NEL
		10/12/2012	529	NEL
		06/12/2012	525	NEL
HZMB 073		09/05/2013	647	NWL
		01/04/2013	623	NWL
		01/04/2013	621	NWL
		21/02/2013	594	NEL
		10/12/2012	529	NEL
		06/12/2012	525	NEL
HZMB 072		24/10/2012	476	NWL
HZMB 071		24/10/2012	475	NWL
		12/10/2012	466	NWL
HZMB 070		24/10/2012	476	NWL
HZMB 069		04/06/2015	1116	NWL
		21/08/2013	774	NWL
		08/07/2013	711	NWL
		24/10/2012	476	NWL
HZMB 068		20/10/2014	1025	NWL
		01/11/2013	839	NWL
		24/10/2012	476	NWL
HZMB 067		24/10/2012	475	NWL
HZMB 066	NL93	28/01/2013	559	NWL
		11/12/2012	537	NWL
		24/10/2012	475	NWL
		12/10/2012	466	NWL
		07/11/2011	Baseline	NWL
		05/11/2011	Baseline	NWL
HZMB 064		19/03/2015	1086	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		17/06/2014	964	NWL
		09/05/2013	647	NWL
		28/01/2013	561	NWL
		24/10/2012	475	NWL
		12/10/2012	466	NWL
HZMB 063		09/05/2013	647	NWL
		12/10/2012	466	NWL
HZMB 062		06/12/2012	525	NEL
		11/10/2012	457	NWL
HZMB 060		18/09/2012	447	NWL
HZMB 059		21/02/2013	591	NWL
		18/09/2012	445	NWL
HZMB 057		18/09/2012	440	NWL
HZMB 056		18/09/2012	442	NWL
		05/09/2012	433	NEL
HZMB 055		04/09/2012	425	NWL
HZMB 054	CH34	20/04/2015	1097	NWL
		15/01/2015	1062	NWL
		31/05/2014	953	NWL
		06/01/2014	888	NWL
		07/11/2013	854	NWL
		02/11/2013	845	NWL
		24/10/2013	831	NWL
		30/08/2013	780	NEL
		08/07/2013	711	NWL
		18/09/2013	448	NWL
		05/09/2012	432	NEL
		07/11/2011	Baseline	NWL
		05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		01/11/2011	Baseline	NEL
		01/11/2011	Baseline	NEL
		28/10/2011	Baseline	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		06/10/2011	Baseline	NWL
HZMB 053		04/09/2012	425	NWL
HZMB 052		04/09/2012	423	NWL
HZMB 051	NL213	11/05/2015	1104	NWL
		04/08/2014	989	NWL
		09/05/2013	644	NWL
		01/04/2013	622	NWL
		15/02/2013	582	NWL
		15/02/2013	581	NWL
		28/01/2013	559	NWL
		28/01/2013	556	NWL
		04/09/2012	422	NWL
HZMB 050		14/07/2014	971	NWL
		10/01/2014	900	NWL
		06/01/2014	888	NWL
		15/02/2013	579	NWL
		04/09/2012	421	NWL
HZMB 049		09/10/2015	1151	NWL
		29/07/2014	982	NWL
		03/09/2012	419	NWL
HZMB 048		03/09/2012	419	NWL
HZMB 047		28/04/2015	1100	NWL
		03/09/2012	412	NWL
HZMB 046		03/09/2012	412	NWL
HZMB 045		17/02/2014	910	NWL
		13/06/2013	682	NWL
		15/02/2013	579	NWL
		01/11/2012	495	NWL
HZMB 044	NL98	13/10/2014	1019	NWL
		17/02/2014	910	NWL
		19/12/2013	864	NWL
		02/11/2013	845	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		01/11/2013	842	NWL
		15/10/2013	819	NWL
		09/05/2013	648	NWL
		09/05/2013	647	NWL
		01/04/2013	623	NWL
		01/04/2013	621	NWL
		15/02/2013	579	NWL
		01/11/2012	495	NWL
		07/11/2011	Baseline	NWL
		06/11/2011	Baseline	NEL
		01/11/2011	Baseline	NEL
		06/10/2011	Baseline	NEL
HZMB 043		03/09/2012	407	NWL
HZMB 042	NL260	22/10/2015	1156	NWL
		19/12/2013	863	NWL
		01/11/2012	495	NWL
		07/11/2011	Baseline	NWL
HZMB 041	NL24	05/06/2014	960	NEL
		17/02/2014	910	NWL
		02/11/2013	845	NWL
		09/05/2013	648	NWL
		09/05/2013	647	NWL
		01/04/2013	623	NWL
		01/04/2013	621	NWL
		15/02/2013	579	NWL
		01/11/2012	495	NWL
		06/11/2011	Baseline	NEL
		05/11/2011	Baseline	NWL
		05/11/2011	Baseline	NWL
		10/10/2011	Baseline	NWL
HZMB 040		17/02/2014	910	NWL
		06/01/2014	893	NWL
		15/10/2013	821	NWL
		08/07/2013	714	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		08/07/2013	711	NWL
		21/02/2013	589	NWL
		01/11/2012	493	NWL
HZMB 038		01/11/2012	490	NWL
HZMB 037		01/11/2012	490	NWL
HZMB 036		03/09/2012	407	NWL
		01/11/2012	490	NWL
HZMB 035		15/02/2013	579	NWL
		01/11/2012	490	NWL
HZMB 034		01/11/2012	493	NWL
HZMB 028		17/11/2014	1035	NWL
		01/04/2013	625	NWL
		06/08/2012	373	NWL
HZMB 027		19/12/2013	863	NWL
		15/02/2013	579	NWL
		28/01/2013	568	NWL
		28/01/2013	564	NWL
		14/06/2012	299	NWL
HZMB 026		13/10/2014	1018	NWL
		25/06/2013	697	NWL
		09/05/2013	642	NWL
		28/01/2013	561	NWL
		13/06/2012	295	NEL
HZMB 025		22/02/2013	596	NEL
		21/02/2013	591	NWL
		06/12/2012	525	NEL
		11/10/2012	457	NWL
		13/06/2012	295	NEL
HZMB 024		18/03/2013	601	NWL
		13/06/2012	295	NEL
HZMB 023		09/10/2015	1153	NWL
		09/10/2015	1152	NWL
		20/04/2015	1097	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		18/12/2014	1044	NWL
		17/11/2014	1035	NWL
		06/01/2014	888	NWL
		08/07/2013	715	NWL
		08/07/2013	711	NWL
		01/04/2013	619	NWL
		21/02/2013	589	NWL
		15/02/2013	579	NWL
		10/07/2012	330	NWL
HZMB 022		09/07/2015	1143	NWL
		20/04/2015	1097	NWL
		18/12/2014	1044	NWL
		17/11/2014	1035	NWL
		04/08/2014	991	NWL
		06/01/2014	888	NWL
		24/10/2013	827	NWL
		08/07/2013	715	NWL
		08/07/2013	711	NWL
		01/04/2013	619	NWL
		21/02/2013	589	NWL
		15/02/2013	579	NWL
		10/07/2012	330	NWL
		HZMB 021	NL37	10/07/2012
16/09/2011	Baseline			NWL
HZMB 020		10/07/2012	330	NWL
HZMB 019		10/07/2012	330	NWL
HZMB 018		17/02/2014	910	NWL
		09/05/2013	647	NWL
		21/02/2013	594	NEL
		10/12/2012	529	NEL
		10/07/2012	330	NWL
HZMB 017		10/07/2012	330	NWL
HZMB 016		08/07/2013	706	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		11/12/2012	539	NWL
		18/09/2012	446	NWL
		04/09/2012	421	NWL
		10/07/2012	330	NWL
HZMB 015		10/07/2012	330	NEL
HZMB 014	NL176	25/08/2015	1139	NWL
		26/12/2013	880	NWL
		06/08/2012	373	NWL
		13/06/2012	295	NEL
		06/11/2011	Baseline	NEL
		01/11/2011	Baseline	NEL
		01/11/2011	Baseline	NEL
HZMB 013		28/05/2012	281	NWL
HZMB 012		28/05/2012	281	NWL
HZMB 011	EL01	22/02/2013	597	NEL
		21/02/2013	592	NEL
		14/02/2013	572	NEL
		06/11/2012	517	NEL
		19/09/2012	452	NWL
		31/03/2012	261	NEL
		02/11/2011	Baseline	NWL
		01/11/2011	Baseline	NEL
HZMB 009		19/03/2015	1084	NWL
		28/05/2012	281	NWL
HZMB 008		06/07/2015	1122	NWL
		28/05/2012	281	NWL
HZMB 007	NL246	10/12/2012	529	NEL
		06/11/2011	Baseline	NEL
		16/09/2011	Baseline	NWL
HZMB 006		22/10/2015	1158	NWL
		21/02/2013	594	NEL
		11/12/2012	539	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		01/11/2012	495	NWL
		29/03/2012	250	NWL
HZMB 005		09/02/2015	1070	NWL
		09/02/2015	1069	NWL
		09/11/2013	860	NWL
		07/11/2013	858	NWL
		15/10/2013	813	NWL
		10/12/2012	532	NWL
		06/08/2012	374	NWL
		28/05/2012	287	NWL
HZMB 004		28/07/2015	1126	NWL
		04/09/2012	421	NWL
		31/03/2012	262	NWL
HZMB 003	NL179	15/10/2013	812	NWL
		25/06/2013	697	NWL
		10/12/2012	529	NEL
		31/03/2012	261	NWL
		06/11/2011	Baseline	NEL
		16/09/2011	Baseline	NWL
HZMB 002	WL111	31/05/2014	951	NWL
		26/12/2013	878	NWL
		19/12/2013	863	NWL
		01/11/2013	839	NWL
		15/10/2013	819	NWL
		24/09/2013	798	NWL
		14/02/2013	573	NWL
		11/12/2012	536	NWL
		11/12/2012	535	NWL
		12/10/2012	466	NWL
		24/10/2012	475	NWL
		28/05/2012	281	NWL
		29/03/2012	250	NWL
		02/11/2011	Baseline	NWL
HZMB 001	WL46	25/08/2014	997	NWL
		21/08/2013	771	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		13/06/2013	681	NWL
		01/04/2013	617	NWL
		14/02/2013	573	NWL
		29/03/2012	250	NWL
	CH98	02/11/2011	Baseline	NWL
	NL11	02/11/2011	Baseline	NWL
		07/11/2011	Baseline	NWL
	NL12	02/11/2011	Baseline	NWL
	NL33	23/09/2011	Baseline	NWL
		01/11/2011	Baseline	NEL
		05/11/2011	Baseline	NWL
		07/11/2011	Baseline	NWL
	NL46	28/10/2011	Baseline	NWL
	CH153	11/10/2011	Baseline	NWL
	NL48	07/11/2001	Baseline	NWL
		02/11/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
	NL75	16/09/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
		01/11/2011	Baseline	NEL
	NL80	02/11/2011	Baseline	NWL
	NL118	06/09/2011	Baseline	NWL
	NL120	06/11/2011	Baseline	NEL
		10/10/2011	Baseline	NWL
	NL123	06/11/2011	Baseline	NEL
		10/10/2011	Baseline	NWL
		06/10/2011	Baseline	NWL
	NL139	01/11/2011	Baseline	NEL
		10/10/2011	Baseline	NEL
		16/09/2011	Baseline	NWL
	NL165	05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
	NL170	06/10/2011	Baseline	NEL
	NL188	07/11/2011	Baseline	NWL
		01/11/2011	Baseline	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		28/10/2011	Baseline	NWL
	NL191	07/09/2011	Baseline	NWL
	NL202	07/11/2011	Baseline	NWL
		28/10/2011	Baseline	NWL
	NL210	07/11/2011	Baseline	NWL
		05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		07/09/2011	Baseline	NWL
	NL214	05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		28/10/2011	Baseline	NWL
	NL220	10/10/2011	Baseline	NEL
	NL224	28/10/2011	Baseline	NWL
	NL226	05/11/2011	Baseline	NWL
		17/10/2011	Baseline	WL
	NL230	02/11/2011	Baseline	NWL
		17/10/2011	Baseline	WL
	NL233	28/10/2011	Baseline	NWL
		06/10/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
	NL241	07/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
	NL244	01/11/2011	Baseline	NEL
		01/11/2011	Baseline	NWL
		05/09/2011	Baseline	WL
	NL256	02/11/2011	Baseline	NWL
	NL258	16/09/2011	Baseline	NWL
		05/09/2011	Baseline	WL
	NL259	07/11/2011	Baseline	NWL
	NL261	01/11/2011	Baseline	NEL
	NL264	06/11/2011	Baseline	NEL
		06/10/2011	Baseline	NEL
		23/09/2011	Baseline	NWL
	NL269	02/11/2011	Baseline	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
	NL272	05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		28/10/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
	NL278	02/11/2011	Baseline	NWL
	NL279	02/11/2011	Baseline	NWL
	SL42	02/11/2011	Baseline	NWL
	SL43	28/10/2011	Baseline	NWL
	WL04	05/11/2011	Baseline	NWL
		02/11/2011	Baseline	NWL
		17/10/2011	Baseline	WL
		10/10/2011	Baseline	NWL
		16/09/2011	Baseline	NWL
	WL05	01/11/2011	Baseline	NEL
		01/11/2011	Baseline	NEL
	WL11	07/11/2011	Baseline	NWL
	WL25	17/10/2011	Baseline	WL
		23/09/2011	Baseline	WL
		16/09/2011	Baseline	NWL
	WL88	02/11/2011	Baseline	WL
		16/09/2011	Baseline	NWL
	WL116	16/09/2011	Baseline	NWL
	WL124	02/11/2011	Baseline	NWL
	WL156	28/10/2011	Baseline	NWL
		23/09/2011	Baseline	WL
	WL162	16/09/2011	Baseline	NWL
	NL275	23/09/2011	Baseline	WL
	SL48	02/11/2011	Baseline	WL
		17/10/2011	Baseline	WL
		23/09/2011	Baseline	WL
	CH108	02/11/2011	Baseline	WL
		02/11/2011	Baseline	WL
	CH157	02/11/2011	Baseline	WL
	NL206	07/10/2011	Baseline	WL
	WL28	23/09/2011	Baseline	WL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
	WL42	02/11/2011	Baseline	WL
		05/09/2011	Baseline	WL
	WL47	17/10/2011	Baseline	WL
	WL61	17/10/2011	Baseline	WL
		23/09/2011	Baseline	WL
	WL66	07/11/2011	Baseline	WL
	WL68	05/09/2011	Baseline	WL
		05/09/2011	Baseline	WL
	WL72	02/11/2011	Baseline	WL
		02/11/2011	Baseline	WL
		23/09/2011	Baseline	WL
	WL87	23/09/2011	Baseline	WL
	WL88	02/11/2011	Baseline	WL
		16/09/2011	Baseline	WL
	WL116	16/09/2011	Baseline	WL
	WL118	02/11/2011	Baseline	WL
		02/11/2011	Baseline	WL
	WL123	02/11/2011	Baseline	WL
	WL124	02/11/2011	Baseline	WL
	WL128	07/11/2011	Baseline	WL
		02/11/2011	Baseline	WL
	WL131	02/11/2011	Baseline	WL
		02/11/2011	Baseline	WL
		23/09/2011	Baseline	WL
	WL132	23/09/2011	Baseline	WL
	WL137	02/11/2011	Baseline	WL
	WL138	02/11/2011	Baseline	WL
	WL144	02/11/2011	Baseline	WL
	WL145	05/09/2011	Baseline	WL
	WL146	17/10/2011	Baseline	WL
	WL153	07/11/2011	Baseline	WL
	WL157	23/09/2011	Baseline	WL
	WL158	23/09/2011	Baseline	WL
	WL163	07/11/2011	Baseline	WL
		02/11/2011	Baseline	WL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
	WL165	17/10/2011	Baseline	WL
	WL167	17/10/2011	Baseline	WL
	WL170	07/11/2011	Baseline	WL
	WL171	28/10/2011	Baseline	WL

HZMB 114 LL 2015-11-05 09-40-15 MED



HZMB 114 LL 2015-11-05 09-42-42 MED



Appendix L – Event Action Plan

Event / Action Plan for Air Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event / Action Plan for Construction Noise

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Inform IEC, ER, EPD and Contractor; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event / Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat <i>in situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Repeat measurement on next day of exceedance to confirm findings. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working methods; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of non-compliance in writing; 2. Discuss with IEC on the proposed mitigation measures; 3. Make agreement on mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET and IEC on possible remedial actions and propose mitigation measures to IEC and ER; 5. Implement the agreed mitigation measures. 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Action level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat <i>in situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Action level; 8. Repeat measurement on next day of exceedance to confirm findings. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of non-compliance in writing; 2. Discuss with IEC on the proposed mitigation measures; 3. Make agreement on mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented; 5. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET and IEC on possible remedial actions and propose mitigation measures to IEC and ER within 3 working days of notification; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat <i>in-situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 3. Request Contractor to critically review the working methods; 4. Ensure mitigation measures are properly implemented; 5. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat <i>in-situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the Contractor's mitigation measures whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 3. Request Contractor to critically review the working methods; 4. Make agreement on the mitigation measures to be implemented; 5. Ensure mitigation measures are properly implemented; 6. Assess the effectiveness of the implemented mitigation measures; 7. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Take immediate action to avoid further exceedance; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 6. Implement the agreed mitigation measures; 7. Resubmit proposals of mitigation measures if problem still not under control; 8. As directed by the Engineer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.

Event / Action Plan for Dolphin Monitoring

Event	ET Leader	IEC	ER / SOR	Contractor
Action Level	<ol style="list-style-type: none"> 1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor; 5. Check monitoring data. 6. Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and finding with the ET and the Contractor. 	<ol style="list-style-type: none"> 1. Discuss monitoring with the IEC and any other measures proposed by the ET; 2. If ER/SOR is satisfied with the proposal of any other measures, ER/SOR to signify the agreement in writing on the measures to be implemented. 	<ol style="list-style-type: none"> 1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER/SOR; 3. Implement the agreed measures.
Limit Level	<ol style="list-style-type: none"> 1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor of findings; 5. Check monitoring data; 6. Repeat review to ensure all the 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and findings with the ET and the Contractor; 3. Attend the meeting to discuss with ET, ER/SOR and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 4. Review proposals for additional monitoring and any other mitigation measures submitted by ET and Contractor and 	<ol style="list-style-type: none"> 1. Attend the meeting to discuss with ET, IEC and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 2. If ER/SOR is satisfied with the proposals for additional dolphin monitoring and/or any other mitigation measures submitted by ET and Contractor and verified by IEC, ER/SOR to signify the agreement in writing on such proposals and any other mitigation measures. 3. Supervise the implementation 	<ol style="list-style-type: none"> 1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Attend the meeting to discuss with ET, IEC and ER/SOR the necessity of additional dolphin monitoring and any other potential mitigation measures. 3. Jointly submit with ET to IEC a proposal of additional dolphin monitoring and/or any other mitigation measures when necessary. 4. Implement the agreed additional dolphin monitoring and/or any other mitigation

	<p>dolphin protective measures are fully and properly implemented and advise on additional measures if necessary.</p> <p>7. If ET proves that the source of impact is caused by any of the construction activity by the works contract, ET to arrange a meeting to discuss with IEC, ER/SOR and Contractor the necessity of additional dolphin monitoring and/or any other potential mitigation measures (e.g., consider to modify the perimeter silt curtain or consider to control/temporarily stop relevant construction activity etc.) and submit to IEC a proposal of additional dolphin monitoring and/or mitigation measures where necessary.</p>	<p>advise ER/SOR of the results and findings accordingly.</p> <p>5. Supervise / Audit the implementation of additional monitoring and/or any other mitigation measures and advise ER/SOR the results and findings accordingly.</p>	<p>of additional monitoring and/or any other mitigation measures.</p>	<p>measures.</p>
--	--	--	---	------------------



China Harbour Engineering Company Limited

Monthly Summary Waste Flow Table for December / 2015 (year)

Project : Hong Kong – Zhuhai – Macao Bridge, Hong Kong Boundary Crossing Facilities – Reclamation Works

Contract No.: HY/2010/02

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste (see Note 4)	Others, e.g. general refuse (see Note 3)
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Jan-15	0.0000	0.0000	0.0000	0.0000	0.0000	1774.7845	0.0000	0.4200	4.0000	2.4000	0.0455
Feb-15	0.0000	0.0000	0.0000	0.0000	0.0000	1120.6675	0.0000	0.1400	0.0000	0.0000	0.0390
Mar-15	0.0000	0.0000	0.0000	0.0000	0.0000	390.8735	0.0040	0.3340	0.0020	0.0000	0.0390
Apr-15	0.0000	0.0000	0.0000	0.0000	0.0000	251.3183	0.0000	0.1400	0.0000	0.0000	0.0390
May-15	0.0000	0.0000	0.0000	0.0000	0.0000	778.9842	0.0000	0.1960	0.0000	0.0000	0.0260
Jun-15	0.0000	0.0000	0.0000	0.0000	0.0000	400.6428	0.0000	0.1680	0.0000	0.0000	0.0520
Sub-total	0.0000	0.0000	0.0000	0.0000	0.0000	4717.2709	0.0040	1.3980	4.0020	2.4000	0.2405
Jul-15	0.0000	0.0000	0.0000	0.0000	0.0000	60.7108	0.0150	0.4750	0.0020	0.0000	0.0585
Aug-15	0.0000	0.0000	0.0000	0.0000	0.0000	60.6718	0.0000	0.3360	5.1200	0.0000	0.0585
Sep-15	0.0000	0.0000	0.0000	0.0000	0.0000	69.8487	0.0000	0.0000	0.0000	0.0000	0.0780
Oct-15	0.0000	0.0000	0.0000	0.0000	0.0000	32.4733	0.0000	0.2800	0.0000	0.0000	0.0715
Nov-15	0.0000	0.0000	0.0000	0.0000	0.0000	40.5700	0.0000	0.3920	0.0000	0.0000	0.0715
Dec-15	0.0000	0.0000	0.0000	0.0000	0.0000	23.0400	0.0000	0.0000	0.0000	0.0000	0.0845
Total	0.0000	0.0000	0.0000	0.0000	0.0000	5004.5856	0.0190	2.8810	9.1240	2.4000	0.6630

Notes: (1) Broken concrete for recycling into aggregates.

(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.

(3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m³ by volume.

(4) Chemical waste refer to spent “battery” and “oil with water”.

Appendix N

Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics on Exceedances

		Total no. recorded in this month	Total no. recorded since project commencement
1-Hour TSP	Action	-	-
	Limit	-	-
24-Hour TSP	Action	-	-
	Limit	-	-
Noise	Action	-	-
	Limit	-	-
Water Quality	Action	-	2
	Limit	-	3
Dolphin Monitoring	Action	-	-
	Limit	-	-

Remarks: Exceedances which are not project-related are not presented in this table.

Cumulative statistics on Complaints, Notifications of Summons and Successful Prosecutions

	Date Received	Subject	Status	Total no. received in this month	Total no. received since project commencement
Environmental complaints	4 December 2015	A water quality complaint was referred to the ENPO at 10:22 am on the 4 December 2015 by EPD; ENPO referred this complaint to this Contract on the same day. With referred to the information provided by ENPO, EPD has contacted the complainant, and obtained the additional information from the complainant and it is suspected that the incident happened in the afternoon on 28 November 2015. A video was provided by	Closed	1	35

		the complainant who shows that turbid water behind a barge, the incident is suspected to be happened in the afternoon on 28 November 2015. After investigation, it is considered not related to this Contract.			
Notification of summons	-	-	-	-	2
Successful Prosecutions	-	-	-	-	2
