



JOB No.: TCS00694/13

**AGREEMENT NO. CE 45/2008 (CE)
LIANTANG/HEUNG YUEN WAI
BOUNDARY CONTROL POINT AND ASSOCIATED WORKS**

**MONTHLY ENVIRONMENTAL MONITORING AND AUDIT
REPORT (NO.62) – SEPTEMBER 2018**

**PREPARED FOR
CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
(CEDD)**

Date	Reference No.	Prepared By	Certified By
12 October 2018	TCS00694/13/600/R1810v3	 Nicola Hon (Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	8 October 2018	First Submission
2	11 October 2018	Amended according to the IEC's comments on 8 October 2018
3	12 October 2018	Amended according to the IEC's comments on 11 October 2018



Member of the Surbana Jurong Group

local people
global experience

Our ref: 7076192/L23595/AB/AW/MCC/rw

12 October 2018

AECOM
8/F, Grand Central Plaza, Tower 2
138 Shatin Rural Committee Road
Shatin, N.T.

By Email & Post

Attention: Mr Simon LEUNG

Dear Sir

**Agreement No. CE 45/2008 (CE)
Liantang/Heung Yuen Wai Boundary Control Point and Associated Works
Independent Environmental Checker – Investigation
Monthly EM&A Report (No. 62) – September 2018**

With reference to the Monthly EM&A Report No. 62 for September 2018 (Version 3) certified by the ET Leader, please be noted that we have no adverse comments on the captioned submission. We herewith verify the captioned submission in accordance with Condition 5.4 of the Environmental Permit No. EP-404/2011/D.

Thank you for your attention and please do not hesitate to contact the undersigned on tel. 3995-8120 or by email to antony.wong@smec.com; or our Mr Arthur CHIU on tel. 3995-8144 or by email to arthur.chiu@smec.com.

Yours faithfully

Antony WONG

Independent Environmental Checker

cc	CEDD/BCP	-	Mr LU Pei Yu / Mr William CHEUNG	by fax: 3547 1659
	ArchSD	-	Mr William WL CHENG	by fax: 2804 6805
	AECOM	-	Mr Pat LAM / Mr Perry YAM	by email
	Ronald Lu	-	Mr Peter YAM / Mr Justin CHEUNG	by email
	CW	-	Mr Daniel HO	by email
	DHK	-	Mr Daniel ALTIER	by email
	CCKJV	-	Mr Vincent CHAN	by email
	KRSJV	-	Mr Matthew TSANG	by email
	Leighton	-	Mr Ray HO	by email
	Siemens	-	Mr Patrick LEUNG	by email
	AUES	-	Mr TW TAM	by email

SMEC ASIA LIMITED
27/F Ford Glory Plaza
37-39 Wing Hong Street
Cheung Sha Wan, Kowloon, Hong Kong
T +852 3995 8100 F +852 3995 8101 E hongkong@smec.com
www.smec.com



EXECUTIVE SUMMARY

ES01 This is the 62nd monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1 to 30 September 2018** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES02 To facilitate the project management and implementation, Liantang/Heung Yuen Wai Boundary Control Point and Associated Works of the Project is divided to seven CEDD contracts including Contract 2 (CV/2012/08), Contract 3 (CV/2012/09), Contract 4 (NE/2014/02), Contract 5 (CV/2013/03), Contract 6 (CV/2013/08) and Contract 7 (NE/2014/03) and an ArshSD contract (Contract SS C505).

ES03 In the Reporting Period, the major construction works under Liantang/Heung Yuen Wai Boundary Control Point and Associated Works of the Project included Contract 2, Contract 3, Contract 4, Contract 6, Contract 7 and Contract SS C505. Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Reporting Period	
		Number of Monitoring Locations to undertake	Total Occasions
Air Quality	1-hour TSP	9	135
	24-hour TSP	9	50
Construction Noise	L _{eq(30min)} Daytime	10	40
Water Quality	Water in-situ measurement and/or sampling	WM1 & WM1-C	13 Scheduled & 0 extra
		WM2A(a) & WM2A-Cx	13 Scheduled & 4 extra
		WM2B & WM2B-C	13 Scheduled & 0 extra (*)
		WM3x & WM3-C	13 Scheduled & 0 extra
		WM4, WM4-CA & WM4-CB	13 Scheduled & 0 extra
Ecology	Woodland compensation i) General Health condition of planted species ii) Survival of planted species	9 Quadrats and transect	0
Joint Site Inspection / Audit	IEC, ET, the Contractor and RE joint site Environmental Inspection and Auditing	Contract 2	4
		Contract 3	4
		Contract 4	4
		Contract 6	4
		Contract 7	4
		Contract SS C505 (#)	4

Remark: (#) IEC only joined one (1) event of site inspection for Contract SS C505.

(*) In the whole Reporting Period, water sampling was unable to carry out at WM2B and WM2B-C due to shallow water (water depth under 150mm)

ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE

ES04 In the Reporting Period, no air quality and construction noise exceedance and valid noise complaint was recorded. For water quality monitoring, a total of ten (10) Action/ Limit Level exceedances were recorded under the Project. The summary of exceedance in the Reporting Period is shown below.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action			
				NOE Issued	Investigation Result	Project related exceedance	Corrective Actions
Air Quality	1-hour TSP	0	0	0	--	--	--
	24-hour TSP	0	0	0	--	--	--

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action			
				NOE Issued	Investigation Result	Project related exceedance	Corrective Actions
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	--	--	--
Water Quality	DO	0	0	0	-	--	--
	Turbidity	1	3	4	Refer to ES.05		The Contractor should fully implement water quality mitigation measure.
	SS	1	5	6			

ES05 Investigation Reports for water quality exceedances have been conducted by ET accordingly. Investigation report revealed the Contractor had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. It was concluded that the exceedance recorded at WM2A(a) on 3, 5, 7 and 18 September 2018 were not caused by the works under the Project. Furthermore, the investigation for exceedances recorded at WM2A(a) on 24 and 27 September 2018 are still underway by ET and the investigation result will be presented in next Monthly EM&A Report.

ENVIRONMENTAL COMPLAINT

ES06 No environmental complaint was recorded in the Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES07 No environmental summons and prosecutions were recorded in the Reporting Period.

REPORTING CHANGE

ES08 No reporting changes were made in the Reporting Period.

SITE INSPECTION

ES09 In this Reporting Period, joint site inspection to evaluate the site environmental performance at **Contract 2** has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 21 and 28 September 2018**. No non-compliance was noted during the site inspection.

ES10 In the Reporting Period, joint site inspection to evaluate the site environmental performance at **Contract 3** has been carried out by the RE, IEC, ET and the Contractor on **6, 13, 19 and 27 September 2018**. No non-compliance was noted during the site inspection.

ES11 In the Reporting Period, joint site inspection to evaluate the site environmental performance at **Contract 4** has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 21 and 24 September 2018**. No non-compliance was noted.

ES12 In the Reporting Period, joint site inspection to evaluate the site environmental performance at **Contract 6** has been carried out by the RE, IEC, ET and the Contractor on **6, 13, 20 and 27 September 2018**. No non-compliance was noted during the site inspection.

ES13 In the Reporting Period, joint site inspection for **Contract 7** to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 18 and 28 September 2018**. No non-compliance was noted during the site inspection.

ES14 In the Reporting Period, joint site inspection to evaluate the site environmental performance at **Contract SS C505** has been carried out by the RE, ET and the Contractor on **5, 12, 19 and 27 September 2018** in which IEC joined the site inspection on **27 September 2018**. No non-compliance was noted during the site inspection.

FUTURE KEY ISSUES

- ES15 During rainy season, preventive measures for muddy water or other water pollutants from site surface flow to local stream such as Kong Yiu Channel, Ma Wat Channel, Ping Yuen River, Kwan Tei River or public area should be properly maintained. The Contractors should paid special attention on water quality mitigation measures and fully implement according ISEMM of the EM&A Manual, in particular for working areas near Ma Wat Channel and Ping Yuen River.
- ES16 In addition, all effluent discharge shall be ensure to fulfill Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or discharge permits stipulation.
- ES17 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants should be implemented in accordance with the EM&A requirement.
- ES18 Since most of construction sites under the Project are located adjacent to villages, the Contractors should fully implement air quality mitigation measures to reduce construction dust emission.

Table of Contents

1	INTRODUCTION	1
1.1	PROJECT BACKGROUND	1
1.2	REPORT STRUCTURE	1
2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	3
2.1	CONSTRUCTION CONTRACT PACKAGING	3
2.2	PROJECT ORGANIZATION	5
2.3	CONCURRENT PROJECTS	7
2.4	CONSTRUCTION PROGRESS	7
2.5	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	10
3	SUMMARY OF IMPACT MONITORING REQUIREMENTS	15
3.1	GENERAL	15
3.2	MONITORING PARAMETERS	15
3.3	MONITORING LOCATIONS	15
3.4	MONITORING FREQUENCY AND PERIOD	17
3.5	MONITORING EQUIPMENT	18
3.6	MONITORING METHODOLOGY	20
3.7	EQUIPMENT CALIBRATION	22
3.8	DERIVATION OF ACTION/LIMIT (A/L) LEVELS	22
3.9	DATA MANAGEMENT AND DATA QA/QC CONTROL	23
4	AIR QUALITY MONITORING	24
4.1	GENERAL	24
4.2	AIR QUALITY MONITORING RESULTS	24
5	CONSTRUCTION NOISE MONITORING	27
5.1	GENERAL	27
5.2	NOISE MONITORING RESULTS	27
6	WATER QUALITY MONITORING	28
6.1	GENERAL	28
6.2	RESULTS OF WATER QUALITY MONITORING	28
7	ECOLOGY MONITORING	32
7.1	GENERAL	32
8	WASTE MANAGEMENT	33
8.1	GENERAL WASTE MANAGEMENT	33
8.2	RECORDS OF WASTE QUANTITIES	33
9	SITE INSPECTION	34
9.1	REQUIREMENTS	34
9.2	FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	34
10	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	38
10.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTIONS	38
11	IMPLEMENTATION STATUS OF MITIGATION MEASURES	41
11.1	GENERAL REQUIREMENTS	41
11.2	TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	41
11.3	KEY ISSUES FOR THE COMING MONTH	43
12	CONCLUSIONS AND RECOMMENDATIONS	45
12.1	CONCLUSIONS	45
12.2	RECOMMENDATIONS	45

LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACTS
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	IMPACT MONITORING STATIONS - AIR QUALITY
TABLE 3-3	IMPACT MONITORING STATIONS - CONSTRUCTION NOISE
TABLE 3-4	IMPACT MONITORING STATIONS - WATER QUALITY
TABLE 3-5	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-6	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-7	WATER QUALITY MONITORING EQUIPMENT
TABLE 3-8	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-9	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-10	ACTION AND LIMIT LEVELS FOR WATER QUALITY
TABLE 4-1	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM1C
TABLE 4-2	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM2
TABLE 4-3	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM3
TABLE 4-4	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM4B
TABLE 4-5	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM5A
TABLE 4-6	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM6
TABLE 4-7	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM7B
TABLE 4-8	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM8
TABLE 4-9	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS – AM9B
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 6-1	WATER QUALITY MONITORING RESULTS ASSOCIATED OF CONTRACTS 2 AND 3
TABLE 6-2	WATER QUALITY MONITORING RESULTS ASSOCIATED OF CONTRACTS 6 AND SS C505
TABLE 6-3	WATER QUALITY MONITORING RESULTS ASSOCIATED ONLY CONTRACT 6
TABLE 6-4	WATER QUALITY MONITORING RESULTS ASSOCIATED CONTRACTS 2 AND 6
TABLE 6-5	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE RECORDED
TABLE 6-6	SUMMARY OF WATER QUALITY EXCEEDANCE IN THE REPORTING PERIOD
TABLE 8-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS FOR THE PROJECT
TABLE 8-2	SUMMARY OF QUANTITIES OF C&D WASTES FOR THE PROJECT
TABLE 9-1	SITE OBSERVATIONS FOR CONTRACT 2
TABLE 9-2	SITE OBSERVATIONS FOR CONTRACT 3
TABLE 9-3	SITE OBSERVATIONS FOR CONTRACT 4
TABLE 9-4	SITE OBSERVATIONS FOR CONTRACT 6
TABLE 9-5	SITE OBSERVATIONS FOR CONTRACT SS C505
TABLE 9-6	SITE OBSERVATIONS FOR CONTRACT 7
TABLE 10-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 10-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 10-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTIONS
TABLE 11-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION CHART
APPENDIX C	3-MONTH ROLLING CONSTRUCTION PROGRAM
APPENDIX D	DESIGNATED MONITORING LOCATIONS AS RECOMMENDED IN THE APPROVED EM&A MANUAL
APPENDIX E	MONITORING LOCATIONS FOR IMPACT MONITORING
APPENDIX F	CALIBRATION CERTIFICATE OF MONITORING EQUIPMENT AND HOKLAS-ACCREDITATION CERTIFICATE OF THE TESTING LABORATORY
APPENDIX G	EVENT AND ACTION PLAN
APPENDIX H	IMPACT MONITORING SCHEDULE
APPENDIX I	DATABASE OF MONITORING RESULT
APPENDIX J	GRAPHICAL PLOTS FOR MONITORING RESULT
APPENDIX K	METEOROLOGICAL DATA
APPENDIX L	WASTE FLOW TABLE
APPENDIX M	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES
APPENDIX N	INVESTIGATION REPORT FOR EXCEEDANCE
APPENDIX O	INVESTIGATION REPORT FOR COMPLAINT

1 INTRODUCTION

1.1 PROJECT BACKGROUND

- 1.1.1 Civil Engineering and Development Department is the Project Proponent and the Permit Holder of Agreement No. CE 45/2008 (CE) Liantang / Heung Yuen Wai Boundary Control Point and Associated Works, which is a Designated Project to be implemented under Environmental Permit number EP-404/2011/D granted on 20 January 2017.
- 1.1.2 The Project consists of two main components: Construction of a Boundary Control Point (hereinafter referred as “BCP”); and Construction of a connecting road alignment. Layout plan of the Project is shown in *Appendix A*.
- 1.1.3 The proposed BCP is located at the boundary with Shenzhen near the existing Chuk Yuen Village, comprising a main passenger building with passenger and cargo processing facilities and the associated customs, transport and ancillary facilities. The connecting road alignment consists of six main sections:
- 1) Lin Ma Hang to Frontier Closed Area (FCA) Boundary – this section comprises at-grade and viaducts and includes the improvement works at Lin Ma Hang Road;
 - 2) Ping Yeung to Wo Keng Shan – this section stretches from the Frontier Closed Area Boundary to the tunnel portal at Cheung Shan and comprises at-grade and viaducts including an interchange at Ping Yeung;
 - 3) North Tunnel – this section comprises the tunnel segment at Cheung Shan and includes a ventilation building at the portals on either end of the tunnel;
 - 4) Sha Tau Kok Road – this section stretches from the tunnel portal at Wo Keng Shan to the tunnel portal south of Loi Tung and comprises at-grade and viaducts including an interchange at Sha Tau Kok and an administration building;
 - 5) South Tunnel – this section comprises a tunnel segment that stretches from Loi Tung to Fanling and includes a ventilation building at the portals on either end of the tunnel as well as a ventilation building in the middle of the tunnel near Lau Shui Heung;
 - 6) Fanling – this section comprises the at-grade, viaducts and interchange connection to the existing Fanling Highway.
- 1.1.4 Action-United Environmental Services & Consulting has been commissioned as an Independent ET to implement the relevant EM&A program in accordance with the approved EM&A Manual, as well as the associated duties. As part of the EM&A program, the baseline monitoring has carried out between **13 June 2013** and **12 July 2013** for all parameters including air quality, noise and water quality before construction work commencement. The Baseline Monitoring Report summarized the key findings and the rationale behind determining a set of Action and Limit Levels (A/L Levels) from the baseline data. Also, the Project baseline monitoring report which verified by the IEC has been submitted to EPD on **16 July 2013** for endorsement. The major construction works of the Project was commenced on **16 August 2013** in accordance with the EP Section 5.3 stipulation.
- 1.1.5 This is **62nd** monthly EM&A report presenting the monitoring results and inspection findings for reporting period from **1 to 30 September 2018**.

1.2 REPORT STRUCTURE

- 1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-
- | | |
|------------------|---|
| Section 1 | <i>Introduction</i> |
| Section 2 | <i>Project Organization and Construction Progress</i> |
| Section 3 | <i>Summary of Impact Monitoring Requirements</i> |
| Section 4 | <i>Air Quality Monitoring</i> |
| Section 5 | <i>Construction Noise Monitoring</i> |
| Section 6 | <i>Water Quality Monitoring</i> |

Section 7	<i>Ecology Monitoring</i>
Section 8	<i>Waste Management</i>
Section 9	<i>Site Inspections</i>
Section 10	<i>Environmental Complaints and Non-Compliance</i>
Section 11	<i>Implementation Status of Mitigation Measures</i>
Section 12	<i>Conclusions and Recommendations</i>

2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 CONSTRUCTION CONTRACT PACKAGING

2.1.1 To facilitate the project management and implementation, the Project would be divided by the following contracts:

- Contract 2 (CV/2012/08)
- Contract 3 (CV/2012/09)
- Contract 4 (NE/2014/02)
- Contract 5 (CV/2013/03)
- Contract 6 (CV/2013/08)
- Contract 7 (NE/2014/03)
- ArchSD Contract No. SS C505

2.1.2 The details of each contracts is summarized below and the delineation of each contracts is shown in *Appendix A*.

Contract 2 (CV/2012/08)

2.1.3 Contract 2 has awarded in December 2013 and construction work was commenced on 19 May 2014. Major Scope of Work of the Contract 2 is listed below:

- construction of an approximately 5.2km long dual two-lane connecting road (with about 0.4km of at-grade road and 4.8km of tunnel) connecting the Fanling Interchange with the proposed Sha Tau Kok Interchange;
- construction of a ventilation adit tunnel and the mid-ventilation building;
- construction of the north and south portal buildings of the Lung Shan Tunnel and their associated slope works;
- provision and installation of ventilation system, E&M works and building services works for Lung Shan tunnel and Cheung Shan tunnel and their portal buildings;
- construction of Tunnel Administration Building adjacent to Wo Keng Shan Road and the associated E&M and building services works; and
- construction of associated footpath, slopes, retaining structures, drainage, sewerage, waterworks, landscaping works and other ancillary works.

Contract 3 (CV/2012/09)

2.1.4 Contract 3 was awarded in July 2013 and construction work was commenced on 5 November 2013. Major Scope of Work of the Contract 3 is listed below:

- construction of four link roads connecting the existing Fanling Highway and the south portal of the Lung Shan Tunnel;
- realignment of the existing Tai Wo Service Road West and Tai Wo Service Road East;
- widening of the existing Fanling Highway (HyD's entrustment works);
- demolishing existing Kiu Tau vehicular bridge and Kiu Tau footbridge and reconstruction of the existing Kiu Tau Footbridge (HyD's entrustment works); and
- construction of associated footpath, slopes, retaining structures, drainage, sewerage, waterworks, landscaping works and other ancillary works.

Contract 4 (NE/2014/02)

2.1.5 Contract 4 has awarded in mid-April 2016 and construction work was commenced on 2 May 2017. The scope of work of the Contract 4 includes:

- design, supply, delivery, installation, testing and commissioning of a traffic control and surveillance system for the connecting road linking up the Liantang / Heung Yuen Wai Boundary Control Point and the existing Fanling Highway.

Contract 5 (CV/2013/03)

2.1.6 Contract 5 has awarded in April 2013 and construction work was commenced in August 2013. Major Scope of Work of the Contract 5 is listed below:

- site formation of about 23 hectares of land for the development of the BCP;
- construction of an approximately 1.6 km long perimeter road at the BCP including a 175m long depressed road;
- associated diversion/modification works at existing local roads and junctions including Lin Ma Hang Road;
- construction of pedestrian subway linking the BCP to Lin Ma Hang Road;
- provision of resite area with supporting infrastructure for reprovisioning of the affected village houses; and
- construction of associated footpath, slopes, retaining structures, drainage, sewerage, waterworks, landscaping works and other ancillary works.

Contract 6 (CV/2013/08)

2.1.7 Contract 6 has awarded in June 2015 and construction work was commenced on 23 October 2015. Major Scope of Work of the Contract 6 would be included below:

- construction of an approximately 4.6km long dual two-lane connecting road (with about 0.6km of at-grade road, 3.3km of viaduct and 0.7km of tunnel) connecting the BCP with the proposed Sha Tau Kok Road Interchange and the associated ventilation buildings;
- associated diversion/modification works at access roads to the resite of Chuk Yuen Village;
- provision of sewage collection, treatment and disposal facilities for the BCP and the resite of Chuk Yuen Village;
- construction of a pedestrian subway linking the BCP to Lin Ma Hang Road;
- provisioning of the affected facilities including Wo Keng Shan Road garden; and
- construction of associated footpath, slopes, retaining structures, drainage, sewerage, waterworks, landscaping works and other ancillary works.

Contract 7 (NE/2014/03)

2.1.8 Contract 7 has awarded in December 2015 and the construction works of Contract 7 was commenced on 15 February 2016. Major Scope of Work of the Contract 7 would be included below:

- construction of the Hong Kong Special Administrative Region (HKSAR) portion of four vehicular bridge
- construction of one pedestrian bridge crossing Shenzhen (SZ) River (cross boundary bridges)

ArchSD Contract No. SS C505

2.1.9 SS C505 has awarded in July 2015 and construction work was commenced on 1 September 2015. Major Scope of Work of the SS C505 would be included below:

- passenger-related facilities including processing kiosks and examination facilities for private cars and coaches, passenger clearance building and halls, the interior fitting works for the pedestrian bridge crossing Shenzhen River, etc.;
- cargo processing facilities including kiosks for clearance of goods vehicles, customs inspection platforms, X-ray building, etc.;
- accommodation for the facilities inside of the Government departments providing services in connection with the BCP;
- transport-related facilities inside the BCP including road networks, public transport interchange, transport drop-off and pick-up areas, vehicle holding areas and associated road furniture etc;
- a public carpark; and

- other ancillary facilities such as sewerage and drainage, building services provisions and electronic systems, associated environmental mitigation measure and landscape works.

2.2 PROJECT ORGANIZATION

2.2.1 The project organization is shown in *Appendix B*. The responsibilities of respective parties are:

Civil Engineering and Development Department (CEDD)

2.2.2 CEDD is the Project Proponent and the Permit Holder of the EP of the development of the Project and will assume overall responsibility for the project. An Independent Environmental Checker (IEC) shall be employed by CEDD to audit the results of the EM&A works carried out by the ET.

Architectural Services Department (ArchSD)

2.2.3 ArchSD acts as the works agent for Development Bureau (DEVB), for Contract SS C505 Liantang/ Heung Yuen Wai Boundary Control Point (BCP) – BCP Buildings and Associated Facilities.

Environmental Protection Department (EPD)

2.2.4 EPD is the statutory enforcement body for environmental protection matters in Hong Kong.

Ronald Lu & Partners (Hong Kong) Ltd (The Architect)

2.2.5 Ronald Lu & Partners (Hong Kong) Ltd is appointed by ArchSD as an Architect for Contract SS C505 Liantang/ Heung Yuen Wai Boundary Control Point (BCP) – BCP Buildings and Associated Facilities. It responsible for overseeing the construction works of Contract SS C505 and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the Architect with respect to EM&A are:

- Monitor the Contractors' compliance with contract specifications, including the implementation and operation of the environmental mitigation measures and their effectiveness
- Monitor Contractors' and ET's compliance with the requirements in the Environmental Permit (EP) and EM&A Manual
- Facilitate ET's implementation of the EM&A programme
- Participate in joint site inspection by the ET and IEC
- Oversee the implementation of the agreed Event / Action Plan in the event of any exceedance
- Adhere to the procedures for carrying out complaint investigation
- Liaison with DSD, Engineer/Engineer's Representative, ET, IEC and the Contractor of the "Construction of the DSD's Regulation of Shenzhen River Stage 4 (RSR 4)" Project discussing regarding the cumulative impact issues.

Engineer or Engineers Representative (ER)

2.2.6 The ER is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the ER with respect to EM&A are:

- Monitor the Contractors' compliance with contract specifications, including the implementation and operation of the environmental mitigation measures and their effectiveness
- Monitor Contractors's, ET's and IEC's compliance with the requirements in the Environmental Permit (EP) and EM&A Manual
- Facilitate ET's implementation of the EM&A programme
- Participate in joint site inspection by the ET and IEC
- Oversee the implementation of the agreed Event / Action Plan in the event of any exceedance

- Adhere to the procedures for carrying out complaint investigation
- Liaison with DSD, Engineer/Engineer's Representative, ET, IEC and the Contractor of the "Construction of the DSD's Regulation of Shenzhen River Stage 4 (RSR 4)" Project discussing regarding the cumulative impact issues.

The Contractor(s)

- 2.2.7 There will be one contractor for each individual works contract. Once the contractors are appointed, EPD, ET and IEC will be notified the details of the contractor.
- 2.2.8 The Contractor for Contracts under CEDD should report to the ER. For ArchSD Contract, the Contractor should report to the Architect or Architect's Representative (AR). The duties and responsibilities of the Contractor are:
- Comply with the relevant contract conditions and specifications on environmental protection
 - Employ an Environmental Team (ET) to undertake monitoring, laboratory analysis and reporting of EM & A Facilitate ET's monitoring and site inspection activities
 - Participate in the site inspections by the ET and IEC, and undertake any corrective actions
 - Provide information / advice to the ET regarding works programme and activities which may contribute to the generation of adverse environmental impacts
 - Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event / Action Plans
 - Implement measures to reduce impact where Action and Limit levels are exceeded
 - Adhere to the procedures for carrying out complaint investigation

Environmental Team (ET)

- 2.2.9 Once the ET is appointed, the EPD, CEDD, ER, Architect and IEC will be notified the details of the ET.
- 2.2.10 The ET shall not be in any way an associated body of the Contractor(s), and shall be employed by the Project Proponent/Contractor to conduct the EM&A programme. The ET should be managed by the ET Leader. The ET Leader shall be a person who has at least 7 years' experience in EM&A and has relevant professional qualifications. Suitably qualified staff should be included in the ET, and resources for the implementation of the EM&A programme should be allocated in time under the Contract(s), to enable fulfillment of the Project's EM&A requirements as specified in the EM&A Manual during construction of the Project. The ET shall report to the Project Proponent and the duties shall include:
- Monitor and audit various environmental parameters as required in this EM&A Manual
 - Analyse the environmental monitoring and audit data, review the success of EM&A programme and the adequacy of mitigation measures implemented, confirm the validity of the EIA predictions and identify any adverse environmental impacts arising
 - Carry out regular site inspection to investigate and audit the Contractors' site practice, equipment/plant and work methodologies with respect to pollution control and environmental mitigation, and effect proactive action to pre-empt problems
 - Monitor compliance with conditions in the EP, environmental protection, pollution prevention and control regulations and contract specifications
 - Audit environmental conditions on site
 - Report on the environmental monitoring and audit results to EPD, the ER, the Architect, the IEC and Contractor or their delegated representatives
 - Recommend suitable mitigation measures to the Contractor in the case of exceedance of Action and Limit levels in accordance with the Event and Action Plans
 - Liaise with the IEC on all environmental performance matters and timely submit all relevant EM&A proforma for approval by IEC
 - Advise the Contractor(s) on environmental improvement, awareness, enhancement measures etc., on site
 - Adhere to the procedures for carrying out complaint investigation

- Liaison with the client departments, Engineer/Engineer's Representative, ET, IEC and the Contractor(s) of the concurrent projects as listed under Section 2.3 below regarding the cumulative impact issues.

Independent Environmental Checker (IEC)

- 2.2.11 One IEC will be employed for this Project. Once the IEC is appointed, EPD, ER, the Architect and ET will be notified the details of the IEC.
- 2.2.12 The Independent Environmental Checker (IEC) should not be in any way an associated body of the Contractor or the ET for the Project. The IEC should be employed by the Permit Holder (i.e., CEDD) prior to the commencement of the construction of the Project. The IEC should have at least 10 years' experience in EM&A and have relevant professional qualifications. The appointment of IEC should be subject to the approval of EPD. The IEC should:
- Provide proactive advice to the ER and the Project Proponent on EM&A matters related to the project, independent from the management of construction works, but empowered to audit the environmental performance of construction
 - Review and audit all aspects of the EM&A programme implemented by the ET
 - Review and verify the monitoring data and all submissions in connection with the EP and EM&A Manual submitted by the ET
 - Arrange and conduct regular, at least monthly site inspections of the works during construction phase, and ad hoc inspections if significant environmental problems are identified
 - Check compliance with the agreed Event / Action Plan in the event of any exceedance
 - Check compliance with the procedures for carrying out complaint investigation
 - Check the effectiveness of corrective measures
 - Feedback audit results to ET by signing off relevant EM&A proforma
 - Check that the mitigation measures are effectively implemented
 - Verify the log-book(s) mentioned in Condition 2.2 of the EP, notify the Director by fax, within one working day of receipt of notification from the ET Leader of each and every occurrence, change of circumstances or non-compliance with the EIA Report and/or the EP, which might affect the monitoring or control of adverse environmental impacts from the Project
 - Report the works conducted, the findings, recommendation and improvement of the site inspections, after reviewing ET's and Contractor's works, and advices to the ER and Project Proponent on a monthly basis
 - Liaison with the client departments, Engineer/Engineer's Representative, the Architect, ET, IEC and the Contractor of the concurrent projects as listed under Section 2.3 below regarding the cumulative impact issues.

2.3 CONCURRENT PROJECTS

- 2.3.1 The concurrent construction works that may be carried out include, but not limited to, the following:
- (a) Regulation of Shenzhen River Stage IV;
 - (b) Widening of Fanling Highway – Tai Hang to Wo Hop Shek Interchange – Contract No. HY/2012/06;
 - (c) Construction of BCP facilities in Shenzhen.

2.4 CONSTRUCTION PROGRESS

- 2.4.1 In the Reporting Period, the major construction activity conducted under the Project is located in Contracts 2, 3, 6, 7 and SS C505 and they are summarized in below. Moreover, 3-month rolling construction program for all the current contracts is enclosed in **Appendix C**.

Contract 2 (CV/2012/08)

2.4.2 The contract commenced in May 2014. In this Reporting Period, construction activities conducted are listed below:

Mid-Vent Portal	<ul style="list-style-type: none"> • Building fit out and E&M installation • Construction of flexible barrier and permanent drainage • Landscaping works.
North Portal	<ul style="list-style-type: none"> • Construction of retaining wall, permanent drainage and slip road • Tunnel backfilling, VE panel and E&M installation • Construction of tunnel internal structure • Landscaping works • North ventilation building fit out and E&M installation
South Portal	<ul style="list-style-type: none"> • Construction of tunnel internal structure, tunnel backfilling and E&M installation • South ventilation building fit out and E&M installation • Construction of flexible barrier • Landscaping works. • Backfilling and construction of slip road
Admin Building	<ul style="list-style-type: none"> • Building fit out, permanent drainage and E&M installation • Landscaping works

Contract 3 (CV/2012/09)

2.4.3 The Contract commenced in November 2013. In this Reporting Period, construction activities conducted are listed below:

- Cable detection and trial trenches
- Remaining works on new Footbridge
- Noise barrier construction
- Road pavement works
- Water main laying works (on Grade and on bridge deck)
- Installation of Noise barrier steel column & panel, and sign gantry (on Grade and on bridge deck)
- Road Drainage Works
- Construction of retaining wall
- Landscaping works

Contract 4 (NE/2014/02)

2.4.4 The Contract was awarded in mid-April 2016 and the construction work was commenced on 2 May 2017. In this Reporting Period, construction activities conducted are listed below:

- E&M installation at Admin Building
- E&M installation at Ventilation Building
- E&M installation at OHVD & tunnel
- High mast erection
- Cladding installation at Cheung Shan Tunnel
- Sign fabrication & installation

Contract 5 (CV/2013/03)

2.4.5 The construction works under Contract 5 was substantially completed on 31 August 2016.

Contract 6 (CV/2013/08)

2.4.6 Contract 6 has awarded in June 2015 and construction work was commenced on 23 October 2015. In this Reporting Period, construction activities conducted are listed below:

- Bridge construction
- Tunneling Works
- Sewage Treatment Plant Construction

- Tunnel Ventilation Building Construction
- Slip Road/At-grade Road/Periphery Road Construction

Contract 7 (NE/2014/03)

2.4.7 Contract 7 has awarded in December 2015 and construction work was commenced on 15 February 2016. In this Reporting Period, construction activities conducted are listed below:

- Profile barrier construction at Bridges A & E
- Noise barrier construction at Bridge D & E
- Waterproofing works at roof of Bridge C
- Drainage and watermains at perimeter road
- Bitumen pavement perimeter road

Contract SS C505

2.4.8 Contract SS C505 has awarded in July 2015 and construction work was commenced on 1 September 2015. In this Reporting Period, construction activities conducted are listed below:

- Passenger Terminal Building (PTB) G/F - Plant Room Structure Works, Backfilling & Drainage, Under Ground Utilities, Fence Wall and On Grade Slab
- PTB - ABWF Works & MEP Installation - Front/Back of House Area, External Staircases, Hall Block External Façade, Southern Entrance Construction, Major Plant Rooms
- PTB - External Works incl. Building 21-24, M/F External Wall (Ewall), Roof & Upper Roof Roofing Works, Podium Coach Canopy, 21&22 (C&PC KIOSKS) & 23&24 (PC Examination Building & MSRVSS) Superstructure & ABWF Works and MEP Installation, Podium Open Area Waterproofing, Paving, Hard and Soft Landscaping works, Ambulance Canopy / Glazed Canopy
- Bridge C Integrated ABWF and MEP Installation Works (C7 Portion)
- Bldg 1 - C&ED Detector Dog Base Phase 1 - Integrated ABWF & MEP Works Works at G/F & R/F
- Bldg 2 - HKPF Building and Observation Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to 4/F and Observation Tower (including Lift)
- Bldg 3 - Fire Station and Drill Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to UR/F, Drill Tower
- Bldg 4 - Cargo Examination Building (Inbound) Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
- Bldg 5 - Cargo Examination Building (Outbound) Phase 2 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
- Bldg 6 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Inbound) - External Works Fence Wall, Integrated ABWF & MEP Works at G/F to R/F
- Bldg 7 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Outbound) - Integrated ABWF & MEP Works at G/F
- Bldg 8 - MXRVSS (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & R/F
- Bldg 9 - MXRVSS (Outbound) Phase 2 - Structure Works at G/F, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 10 - GV Kiosk (Inbound) Phase 2 - On-Grade Slab, Steel Structure Works, Integrated ABWF and MEP Works at G/F & R/F
- Bldg 11 - GV Kiosk (Outbound) Phase 2 - Steel Structure Works, Integrated ABWF & MEP Works at G/F & R/F
- Bldg 12 - Public Toilets (Inbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 13 - Public Toilets (Outbound) Phase 2 - Structures Works, Integrated ABWF and MEP Works at G/F & R/F
- Bldg 14 - Disinsection Facilities (Inbound) Phase 2 - Integrated ABWF & MEP Works at G/F & Envelope
- Bldg 15 - Disinsection Facilities (Outbound) Phase 2 - Substructure and Structure Works, Integrated ABWF & MEP Works at G/F & Envelope
- Bldg 16 - Weigh Station Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope

- Bldg 17 - EUVSS & Monitoring Room Phase 2 - Structure Works, Integrated ABWF & MEP Works at G/F & R/F
- Bldg 18 - Refuse Collection Point Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 25 - Traffic Control Office (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 26 - Traffic Control Office (Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 27 - Inspection Post Phase 2 - Structure Works, Integrated ABWF and MEP Work at G/F & Envelope
- Bldg 28, 30 & 31 - Guard Booth (Inbound/Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 32 to 35 - Steel Canopies Phase 2 - Structure Works, Integrated ABWF and MEP Works
- Bldg 37 to 40 - Elevated Walkway (E1, E2, E3 & E4) Phase 2 - Structures Works, ABWF and BS Works
- Vehicular bridges 1 to 5 Phase 3 - Retaining walls, Road and Finishes Works
- External Works - CLP Cable & Power ON Transfer room
- External Works - Water Meter Room Connection (Inbound & Outbound)
- External Works - External Utilities, UU works & DSD Inspection
- External Works - Road & Pavement Works
- Landscape - Inbound Area
- Testing & Commissioning (T&C) and FSD Inspection - CBO, FXO, Inbound & Outbound Group Buildings

2.5 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.5.1 In according to the EP, the required documents have submitted to EPD which listed in below:
- Project Layout Plans of Contracts 2, 3, 4, 5, 6, 7 and SS C505
 - Landscape Plan
 - Topsoil Management Plan
 - Environmental Monitoring and Audit Programme
 - Baseline Monitoring Report (TCS00690/13/600/R0030v3) for the Project
 - Waste Management Plan of the Contracts 2, 3, 4, 5, 6, 7 and SS C505
 - Contamination Assessment Plan (CAP) and Contamination Assessment Report (CAR) for Po Kat Tsai, Loi Tung and the workshops in Fanling
 - Vegetation Survey Report
 - Woodland Compensation Plan
 - Habitat Creation Management Plan
 - Wetland Compensation Plan

2.5.2 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project of each contracts are presented in **Table 2-1**.

Table 2-1 Status of Environmental Licenses and Permits of the Contracts

Item	Description	License/Permit Status		
		Ref. no.	Effective Date	Expiry Date
Contract 2				
1	Air pollution Control (Construction Dust) Regulation	Ref No.: 368864	31 Dec 2013	Till Contract ends
2	Chemical Waste Producer Registration	<i>North Portal</i> Waste Producers Number: No.5213-652-D2523-01	25 Mar 2014	Till Contract ends

Item	Description	License/Permit Status			
		Ref. no.	Effective Date	Expiry Date	
		<i>Mid-Vent Portal</i> Waste Producers Number: No.5213-634-D2524-01	25 Mar 2014	Till Contract ends	
		<i>South Portal</i> Waste Producers Number: No.5213-634-D2526-01	9 Apr 2014	Till Contract ends	
3	Water Pollution Control Ordinance - Discharge License	No.WT00018374-2014 (South Portal)	3 Mar 2014	28 Feb 2019	
		No. WT00023063-2015 (North Portal)	18 Dec 2015	31 Mar 2019	
		No.: W5/11392 (Admin Building)	28 Mar 2014	31 Mar 2019	
		No.: WT00025594-2016 (Mid-Vent Portal)	7 Oct 2016	31 Mar 2019	
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7019105	8 Jan 2014	Till Contract ends	
5	Construction Noise Permit	GW-RN0211-18	North Portal	10-May-2018	09-Nov-2018
		GW-RN0212-18		10-May-2018	09-Nov-2018
		GW-RN0307-18		18-Jun-2018	17-Dec-2018
		GW-RN0400-18	Mid Vent	06-Aug-2018	01-Feb-2019
		GW-RN0401-18		06-Aug-2018	31-Jan-2019
		GW-RN0238-18	South Portal	01-Jun-2018	30-Nov-2018
		GW-RN0110-18		22-Mar-2018	21-Sep-2018
		GW-RN0176-18		30-Apr-2018	27-Oct-2018
		GW-RN0253-18		06-Jun-2018	05-Dec-2018
		GW-RN0511-18		30-Sep-2018	25-Mar-2019
		GW-RN0513-18		30-Sep-2018	25-Mar-2019
		GW-RN0176-18	30-Apr-2018	27-Oct-2018	
		GW-RN0142-18	Admin Bldg	5-Apr-2018	27-Sep-2018
		GW-RN0523-18		28-Sep-2018	27-Mar-2019
GW-RN0140-18	Cheung Shan Tunnel	3-Apr-2018	22-Sep-2018		
GW-RN0522-18		26-Sep-2018	22-Mar-2019		
6	Specified Process License (Mortar Plant Operation)	L-3-251(1)	12 Apr 2016	11 Apr 2021	
Contract 3					
1	Air pollution Control (Construction Dust) Regulation	Ref. No: 362101	17 Jul 2013	Till Contract ends	
2	Chemical Waste	Waste Producers Number:		Till Contract	

Item	Description	License/Permit Status		
		Ref. no.	Effective Date	Expiry Date
	Producer Registration	No.:5113-634-C3817-01	7 Oct 2013	ends
3	Water Pollution Control Ordinance - Discharge License	No.:WT00032188 – 2018	20 Sep 2018	31 Aug 2023
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7017914	2 Aug 2013	Till Contract ends
5	Construction Noise Permit	GW-RN0259-18	19 Jun 2018	17 Dec 2018
		GW-RN0305-18	22 Jun 2018	17 Dec 2018
		GW-RN0366-18	9 Jul 2018	18 Dec 2018
		GW-RN0361-18	15 Jul 2018	18 Dec 2018
		GW-RN0388-18	25 Aug 2018	24 Feb 2019
		GW-RN0424-18	01 Sep 2018	21 Feb 2019
		GW-RN0425-18	22 Aug 2018	21 Feb 2019
		GW-RN0454-18	06 Sep 2018	05 Mar 2019
Contract 5				
1	Air pollution Control (Construction Dust) Regulation	Ref. No: 359338	13 May 2013	Till the end of Contract
2	Chemical Waste Producer Registration	Waste Producers Number No.: 5213-642-S3735-01	8 Jun 2013	Till the end of Contract
3	Water Pollution Control Ordinance - Discharge License	No.: W5/1G44/1	8 Jun 13	30 Jun 2018
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7017351	29 Apr 13	Till the end of Contract
Contract 6				
1	Air pollution Control (Construction Dust) Regulation	Ref. No: 390614	29 Jun 2015	Till the end of Contract
2	Chemical Waste Producer Registration	Waste Producers Number No.: 5213-652-C3969-01	31 Aug 2015	Till the end of Contract
3	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7022707	9 Jul 2015	Till the end of Contract

Item	Description	License/Permit Status		
		Ref. no.	Effective Date	Expiry Date
4	Water Pollution Control Ordinance - Discharge License	No.:WT00024574-2016	31 May 2016	31 May 2021
		No.:WT00024576-2016	31 May 2016	31 May 2021
		No.:WT00024742-2016	14 June 2016	30 June 2021
		No.:WT00024746-2016	14 June 2016	30 June 2021
5	Construction Noise Permit	GW-RW0121-18	30 Apr 2018	29 Oct 2018
		GW-RW0481-18	14 Sep 2018	13 Mar 2019
Contract SS C505				
1	Air pollution Control (Construction Dust) Regulation	Ref. No: 390974	13 Jul 2015	Till the end of Contract
2	Chemical Waste Producer Registration	Waste Producer No.: 5213-642-L1048-07	16 Sep 2015	Till the end of Contract
3	Water Pollution Control Ordinance - Discharge License	No.: WT00024865-2016	8 Jul 2016	30 Nov 2020
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7022831	23 Jul 2015	Till the end of Contract
5	Construction Noise Permit	GW-RN0114-18	5 Apr 2018	4 Oct 2018
		GW-RN0198-18	8 May 2018	7 Nov 2018
Contract 7				
1	Air pollution Control (Construction Dust) Regulation	Ref. No: 397015	21 Dec 2015	Till the end of Contract
2	Chemical Waste Producer Registration	Waste Producer No.: 5214-641-K3202-01	24 Mar 2016	Till the end of Contract
3	Water Pollution Control Ordinance - Discharge License	No.: WT00024422-2016	10 May 2016	31 May 2021
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7024129	21 Jan 2016	Till the end of Contract
5	Construction Noise Permit	GW-RN0206-18	8 May 2018	4 Nov 2018
Contract 4				
1	Air pollution Control (Construction Dust) Regulation	Ref. No. 405353	22 July 2016	Till the end of Contract

Item	Description	License/Permit Status		
		Ref. no.	Effective Date	Expiry Date
2	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7024973	13 May 2016	Till the end of Contract

3 SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 The Environmental Monitoring and Audit requirements are set out in the Approved EM&A manual. Environmental issues such as air quality, construction noise and water quality were identified as the key issues during the construction phase of the Project.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

3.2.1 The EM&A program of construction phase monitoring shall cover the following environmental issues:

- Air quality;
- Construction noise; and
- Water quality

3.2.2 A summary of the monitoring parameters is presented in *Table 3-1*.

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 1-hour TSP by Real-Time Portable Dust Meter; and • 24-hour TSP by High Volume Air Sampler.
Noise	<ul style="list-style-type: none"> • $L_{eq(30min)}$ in normal working days (Monday to Saturday) 07:00-19:00 except public holiday; and • 3 sets of consecutive $L_{eq(5min)}$ on restricted hours i.e. 19:00 to 07:00 next day, and whole day of public holiday or Sunday • Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
Water Quality	In-situ Measurements <ul style="list-style-type: none"> • Dissolved Oxygen Concentration (mg/L); • Dissolved Oxygen Saturation (%) ; • Turbidity (NTU); • pH unit; • Water depth (m); and • Temperature (°C).
	Laboratory Analysis <ul style="list-style-type: none"> • Suspended Solids (mg/L)

3.3 MONITORING LOCATIONS

3.3.1 The designated monitoring locations as recommended in the *EM&A Manual* are shown in *Appendix D*. As the access to some of the designated monitoring locations was questionable due to safety reason or denied by the landlords, alternative locations therefore have had proposed. The latest alternative monitoring locations has been updated in the revised EM&A Programme (Rev.7) which approved by EPD on 7 April 2017. Besides, in view of Location AM1b was demolished and returned to the landlord on 27 April 2018, alternative location AM1c was proposed by ET. The proposal for alternative location AM1c which verified by IEC on 5 June 2018 submitted to EPD for approval on 6 June 2018. EPD issued comments on 16 July 2018 and the revised proposal was submitted to EPD on 20 August 2018. Further comment was given from EPD on 13 September 2018 and the proposal is under revision by ET. *Table 3-2*, *Table 3-3* and *Table 3-4* listed the air quality, construction noise and water quality monitoring locations for the Project and a map showing these monitoring stations is presented in *Appendix E*.

Table 3-2 Impact Monitoring Stations - Air Quality

Station ID	Description	Works Area	Related to the Work Contract
AM1b^	Open area at Tsung Yuen Ha Village	BCP	SS C505

Station ID	Description	Works Area	Related to the Work Contract
			Contract 7
AM1c(*)	Open area of Tsung Yuen Ha Village No. 63	BCP	SS C505 Contract 7
AM2	Village House near Lin Ma Hang Road	LMH to Frontier Closed Area	Contract 6
AM3	Ta Kwu Ling Fire Service Station of Ta Kwu Ling Village.	LMH to Frontier Closed Area	Contract 6
AM4b^	House no. 10B1 Nga Yiu Ha Village	LMH to Frontier Closed Area	Contract 6
AM5a^	Ping Yeung Village House	Ping Yeung to Wo Keng Shan	Contract 6
AM6	Wo Keng Shan Village House	Ping Yeung to Wo Keng Shan	Contract 6
AM7b [@]	Loi Tung Village House	Sha Tau Kok Road	Contract 2 Contract 6
AM8	Po Kat Tsai Village No. 4	Po Kat Tsai	Contract 2
AM9b#	Nam Wa Po Village House No. 80	Fanling	Contract 3

Proposal for the change of air quality monitoring location from AM9a to AM9b was submitted to EPD on 4 Nov 2013 after verified by the IEC and it was approved by EPD (EPD's ref.: (15) in EP 2/N7/A/52 Pt.10 dated 8 Nov 2013).

@ Proposal for the change of air quality monitoring location from AM7a to AM7b was submitted to EPD on 4 June 2014 after verified by the IEC. It was approved by EPD (EPD's ref.: (7) in EP 2/N7/A/52 Pt.12 dated 9 Jun 2014).

^ Proposal for change of air quality monitoring locations was enclosed in the updated EM&A Programme which approval by EPD on 29 Mar 2016. Besides, Location AM1b was temporary suspended (24-hour TSP monitoring) since 27 April 2018 as the rented land was demolished and returned to the landlord.

* Proposal for alternative location AM1c which verified by the IEC on 5 June 2018 was submitted to EPD on 6 June 2018. EPD issued comments on 16 July 2018 and the revised proposal was submitted to EPD on 20 August 2018. Further comment was given from EPD on 13 September 2018 and the proposal is under revision by ET.

Table 3-3 Impact Monitoring Stations - Construction Noise

Station ID	Description	Works Area	Related to the Work Contract
NM1	Tsung Yuen Ha Village House No. 63	BCP	SS C505 Contract 7
NM2a#	Village House near Lin Ma Hang Road	Lin Ma Hang to Frontier Closed Area	Contract 6
NM3	Ping Yeung Village House (facade facing northeast)	Ping Yeung to Wo Keng Shan	Contract 6
NM4	Wo Keng Shan Village House	Ping Yeung to Wo Keng Shan	Contract 6
NM5	Village House, Loi Tung	Sha Tau Kok Road	Contract 2, Contract 6
NM6	Tai Tong Wu Village House 2	Sha Tau Kok Road	Contract 2, Contract 6
NM7	Po Kat Tsai Village	Po Kat Tsai	Contract 2
NM8	Village House, Tong Hang	Fanling	Contract 2 Contract 3
NM9	Village House, Kiu Tau Village	Fanling	Contract 3
NM10	Nam Wa Po Village House No. 80	Fanling	Contract 3

Proposal for the change of construction noise monitoring location from NM2 to NM2a was verified by the IEC on 6 May 2016 and was effective on 9 May 2016.

Table 3-4 Impact Monitoring Stations - Water Quality

Station ID	Description	Coordinates of Designated / Alternative Location		Nature of the location	Related to the Work Contract
		Easting	Northing		
WM1	Downstream of Kong Yiu Channel	833 679	845 421	Alternative location located at upstream 51m of the designated location	SS C505 Contract 6
WM1-Control	Upstream of Kong Yiu Channel	834 185	845 917	NA	SS C505 Contract 6
WM2A	Downstream of River Ganges	834 204	844 471	Alternative location located at upstream 81m of the designated location	Contract 6
WM2A(a)*	Downstream of River Ganges	834 191	844 474	Alternative location located at upstream 70m of the designated location	Contract 6
WM2A-Controlx#	Upstream of River Ganges	835 377	844 188	Alternative location located at upstream 160m of the designated location	Contract 6
WM2B	Downstream of River Ganges	835 433	843 397	NA	Contract 6
WM2B-Control	Upstream of River Ganges	835 835	843 351	Alternative location located at downstream 31m of the designated location	Contract 6
WM3x#	Downstream of River Indus	836 206	842 270	Alternative location located at downstream 180m of the designated location	Contract 2 Contract 6
WM3-Control	Upstream of River Indus	836 763	842 400	Alternative location located at downstream 26m of the designated location	Contract 2 Contract 6
WM4	Downstream of Ma Wat Channel	833 850	838 338	Alternative location located at upstream 11m of the designated location	Contract 2 Contract 3
WM4-Control A	Kau Lung Hang Stream	834 028	837 695	Alternative location located at downstream 28m of the designated location	Contract 2 Contract 3
WM4-Control B	Upstream of Ma Wat Channel	833760	837395	Alternative location located at upstream 15m of the designated location	Contract 2 Contract 3

Note: EPD has approved the revised EM&A Programme (Rev.7) which proposed that (1) if the measured water depth of the monitoring station is lower than 150 mm, alternative location based on the criteria were selected to perform water monitoring; and (2) If no suitable alternative location could be found within 15m far from the original location, the sampling at that location will be cancelled since sampling at too far from the designated location could not make a representative sample in accordance with the updated EM&A Programme (Rev. 07) (Section 4.1.4) (EPD ref.: () in EP2/N7/A/52 Ax(1) Pt.20 dated 7 April 2017)

(*) Proposal for the change of water monitoring location from WM2A to WM2A(a) was verified by the IEC and it was approved by EPD. (EPD's ref. (10) in EP 2/N7/A/52 Pt.19)

(#) Proposal for the change of water quality monitoring location (WM3x and WM2A-Cx) was included in the EM&A Programme Rev .05 which approved by EPD on 29 March 2016 (EPD ref.: (3) in EP2/N7/A/52 Ax(1) Pt.19)

3.4 MONITORING FREQUENCY AND PERIOD

The requirements of impact monitoring are stipulated in Sections 2.1.6, 3.1.5 and 4.1.6 of the approved EM&A Manual and presented as follows.

Air Quality Monitoring

3.4.1 Frequency of impact air quality monitoring is as follows:

- 1-hour TSP 3 times every six days during course of works

- 24-hour TSP Once every 6 days during course of works.

Noise Monitoring

3.4.2 One set of $L_{eq(30min)}$ as 6 consecutive $L_{eq(5min)}$ between 0700-1900 hours on normal weekdays and once every week during course of works. If construction work necessary to carry out at other time periods, i.e. restricted time period (19:00 to 07:00 the next morning and whole day on public holidays) (hereinafter referred as “the restricted hours”), additional weekly impact monitoring for $L_{eq(5min)}$ measurement shall be employed during respective restricted hours periods.. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

Water Quality Monitoring

3.4.3 The water quality monitoring frequency shall be 3 days per week during course of works. The interval between two sets of monitoring shall not be less than 36 hours.

3.5 MONITORING EQUIPMENT

Air Quality Monitoring

3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve.

3.5.2 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

3.5.3 All equipment to be used for air quality monitoring is listed in **Table 3-5**.

Table 3-5 Air Quality Monitoring Equipment

Equipment	Model
24-Hr TSP	
High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170*
Calibration Kit	TISCH Model TE-5025A*
1-Hour TSP	
Portable Dust Meter	Sibata LD-3B Laser Dust monitor Particle Mass Profiler & Counter*

* Instrument was used in the Reporting Period and the calibration certificate could be referred in Appendix F.

Wind Data Monitoring Equipment

3.5.4 According to the approved EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:

- 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
- 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
- 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
- 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.

3.5.5 ET has liaised with the landlords of the successful granted HVS installation premises. However, the owners rejected to provide premises for wind data monitoring equipment installation.

3.5.6 Under this situation, the ET proposed alternative methods to obtain representative wind data. Meteorological information as extracted from “the Hong Kong Observatory Ta Kwu Ling Station” is alternative method to obtain representative wind data. For Ta Kwu Ling Station, it is located nearby the Project site. Moreover, this station is located at 15m above mean sea level while its anemometer is located at 13m above the existing ground which in compliance with the general setting up requirement. Furthermore, this station also can be to provide the humidity, rainfall, and air pressure and temperature etc. meteorological information. In Hong Kong of a lot development projects, weather information extracted from Hong Kong Observatory is common alternative method if weather station installation not allowed.

Noise Monitoring

3.5.7 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.5.8 Noise monitoring equipment to be used for monitoring is listed in **Table 3-6**.

Table 3-6 Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	B&K Type 2238 and Rion NL-52*
Calibrator	Rion NC-74* and B&K Type 4231**
Portable Wind Speed Indicator	Testo Anemometer

* Instrument was used in the Reporting Period and the calibration certificate could be referred in Appendix F.

3.5.9 Sound level meters listed above comply with the *International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1)* specifications, as recommended in TM issued under the NCO. The acoustic calibrator and sound level meter to be used in the impact monitoring will be calibrated yearly.

Water Quality Monitoring

3.5.10 DO and water temperature should be measured in-situ by a DO/temperature meter. The instrument should be portable and weatherproof using a DC power source. It should have a membrane electrode with automatic temperature compensation complete with a cable. The equipment should be capable of measuring:

- a DO level in the range of 0-20 mg/l and 0-200% saturation; and
- a temperature of between 0 and 45 degree Celsius.

3.5.11 A portable pH meter capable of measuring a range between 0.0 and 14.0 should be provided to measure pH under the specified conditions accordingly to the APHA Standard Methods.

3.5.12 The instrument should be portable and weatherproof using a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU.

3.5.13 A portable, battery-operated echo sounder or tape measure will be used for the determination of water depth at each designated monitoring station as appropriate.

3.5.14 A water sampler e.g. Kahlsico Water Sampler, which is a transparent PVC cylinder with capacity not less than 2 litres, will be used for water sampling if water depth over than 0.5m. For sampling from very shallow water depths e.g. <0.5 m, water sample collection will be directly from water surface below 100mm use sampling plastic bottle to avoid inclusion of bottom sediment or humus. Moreover, Teflon/stainless steel bailer or self-made sampling buckets maybe used for water sampling. The equipment used for sampling will be depended the sampling location and depth situations.

- 3.5.15 Water samples for laboratory measurement of SS will be collected in high density polythene bottles, packed in ice (cooled to 4 °C without being frozen), and delivered to the laboratory in the same day as the samples were collected.
- 3.5.16 Analysis of suspended solids should be carried out in a HOKLAS or other accredited laboratory. Water samples of about 1L should be collected at the monitoring stations for carrying out the laboratory suspended solids determination. The SS determination work should start within 24 hours after collection of the water samples. The SS analyses should follow the *APHA Standard Methods 2540D* with Limit of Reporting of 2 mg/L.
- 3.5.17 Water quality monitoring equipment used in the impact monitoring is listed in **Table 3-7**. Suspended solids (SS) analysis is carried out by a local HOKLAS-accredited laboratory, namely *ALS Technichem (HK) Pty Ltd*.

Table 3-7 Water Quality Monitoring Equipment

Equipment	Model
Water Depth Detector	Eagle Sonar or tape measures
Water Sampler	A 2-litre transparent PVC cylinder with latex cups at both ends or teflon/stainless steel bailer or self-made sampling bucket
Thermometer & DO meter	YSI Professional Plus /YSI PRO20 Handheld Dissolved Oxygen Instrument/ YSI 550A Multifunctional Meter*/ YSI Professional DSS
pH meter	YSI Professional Plus / AZ8685 pH pen-style meter*/ YSI 6820/ 650MDS/ YSI Professional DSS
Turbidimeter	Hach 2100Q*/ YSI 6820/ 650MDS/ YSI Professional DSS
Sample Container	High density polythene bottles (provided by laboratory)
Storage Container	'Willow' 33-liter plastic cool box with Ice pad

* Instrument was used in the Reporting Period and the calibration certificate could be referred in Appendix F.

3.6 MONITORING METHODOLOGY

1-hour TSP Monitoring

- 3.6.1 The 1-hour TSP monitor was a brand named “Sibata LD-3B Laser Dust monitor Particle Mass Profiler & Counter” which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90° light scattering. The 1-hour TSP monitor consists of the following:
- A pump to draw sample aerosol through the optic chamber where TSP is measured;
 - A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
 - A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.

- 3.6.2 The 1-hour TSP meter is used within the valid period as follow manufacturer’s Operation and Service Manual.

24-hour TSP Monitoring

- 3.6.3 The equipment used for 24-hour TSP measurement is Tisch Environmental, Inc. Model TE-5170 TSP high volume air sampling system, which complied with *EPA Code of Federal Regulation, Appendix B to Part 50*. The High Volume Air Sampler (HVS) consists of the following:
- An anodized aluminum shelter;
 - A 8”x10” stainless steel filter holder;
 - A blower motor assembly;
 - A continuous flow/pressure recorder;

- (e.) A motor speed-voltage control/elapsed time indicator;
- (f.) A 7-day mechanical timer, and
- (g.) A power supply of 220v/50 Hz

- 3.6.4 The HVS is operated and calibrated on a regular basis in accordance with the manufacturer's instruction using Tisch Calibration Kit Model TE-5025A. Calibration would carry out in two month interval.
- 3.6.5 24-hour TSP is collected by the ET on filters of HVS and quantified by a local HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (ALS), upon receipt of the samples. The ET keep all the sampled 24-hour TSP filters in normal air conditioned room conditions, i.e. 70% RH (Relative Humidity) and 25°C, for six months prior to disposal.

Noise Monitoring

- 3.6.6 Noise measurements were taken in terms of the A-weighted equivalent sound pressure level (L_{eq}) measured in decibels dB(A). Supplementary statistical results (L_{10} and L_{90}) were also obtained for reference.
- 3.6.7 During the monitoring, all noise measurements would be performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30min)}$ in six consecutive $L_{eq(5min)}$ measurements will use as the monitoring parameter for the time period between 0700-1900 hours on weekdays; $L_{eq(5min)}$ measurements would be used as monitoring parameter for other time periods (e.g. during restricted hours), if necessary.
- 3.6.8 Prior of noise measurement, the accuracy of the sound level meter is checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The checking is performed before and after the noise measurement.

Water Quality

- 3.6.9 Water quality monitoring is conducted at the designated or alternative locations. The sampling procedures with the in-situ monitoring are presented as below:

Sampling Procedure

- 3.6.10 A Digital Global Positioning System (GPS) is used to identify the designated monitoring stations prior to water sampling. A portable, battery-operated echo sounder or tape measurement is used for the determination of water depth at each station. At each station, water sample would be collected from 0.1m below water surface or the water surface to prevent the river bed sediment for stirring.
- 3.6.11 If the water level of a monitoring station is too shallow when sampling, sediment would be disturbed which affecting the accuracy of water quality monitoring. In order to avoid disturbing sediment, depth limits should be set up for the water sampling for the ease of reference. When the measured water depth of the monitoring station (both control and impact stations) is lower than 150mm, water monitoring would not be to perform at that monitoring location. Instead, the monitoring location will be moved to a temporary alternative location monitoring location based on the criteria below:-
- (a) the alternative location should be either upstream or downstream of the original location and at the same the river/drain channel
 - (b) the alternative location should be within 15m far from the original location
 - (c) if no suitable alternative location could be found within 15m far from the original location, the sampling at that location will be cancelled since sampling at too far from the designated location could not make a representative sample.
- 3.6.12 The sample container will be rinsed with a portion of the water sample. The water sample then will be transferred to the high-density polythene bottles as provided by the laboratory, labeled with a unique sample number and sealed with a screw cap.

- 3.6.13 Before sampling, general information such as the date and time of sampling, weather condition as well as the personnel responsible for the monitoring would be recorded on the field data sheet.
- 3.6.14 A ‘Willow’ 33-liter plastic cool box packed with ice will be used to preserve the water samples prior to arrival at the laboratory for chemical determination. The water temperature of the cool box is maintained at a temperature as close to 4⁰C as possible without being frozen. Samples collected are delivered to the laboratory upon collection.

In-situ Measurement

- 3.6.15 YSI 550A Multifunctional Meter is used for water in-situ measures, which automates the measurements and data logging of temperature, dissolved oxygen and dissolved oxygen saturation.
- 3.6.16 A portable AZ Model 8685 is used for in-situ pH measurement. The pH meter is capable of measuring pH in the range of 0 – 14 and readable to 0.1.
- 3.6.17 A portable Hach 2100Q Turbidimeter is used for in-situ turbidity measurement. The turbidity meter is capable of measuring turbidity in the range of 0 – 1000 NTU.
- 3.6.18 All in-situ measurement equipment are calibrated by HOKLAS accredited laboratory of three month interval.

Laboratory Analysis

- 3.6.19 All water samples analyzed Suspended Solids (SS) will be carried out by a local HOKLAS-accredited testing laboratory (ALS Technichem (HK) Pty Ltd HOKLAS registration no. 66). SS determination using *APHA Standard Methods 2540D* as specified in the *EM&A Manual* will start within 48 hours of water sample receipt.

3.7 EQUIPMENT CALIBRATION

- 3.7.1 Calibration of the HVS is performed upon installation and thereafter at bimonthly intervals in accordance with the manufacturer’s instruction using the certified standard calibrator (TISCH Model TE-5025A). Moreover, the Calibration Kit would be calibrated annually. The calibration data are properly documented and the records are maintained by ET for future reference.
- 3.7.2 The 1-hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment would be checked before and after each monitoring event. Annually calibration with the High Volume Sampler (HVS) in same condition would be undertaken by the Laboratory.
- 3.7.3 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.7.4 All water quality monitoring equipment would be calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.7.5 The calibration certificates of all monitoring equipment used for the impact monitoring program in the Reporting Period and the HOKLAS accredited certificate of laboratory are attached in *Appendix F*.

3.8 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.8.1 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. According to the approved Environmental Monitoring and Audit Manual, the air quality, construction noise and water quality criteria were set up, namely Action and Limit levels are listed in *Tables 3-8, 3-9 and 3-10*.

Table 3-8 Action and Limit Levels for Air Quality Monitoring

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AM1c	265	143	500	260
AM2	268	149		
AM3	269	145		
AM4b	267	148		
AM5a	268	143		
AM6	269	148		
AM7b	275	156		
AM8	269	144		
AM9b	271	151		

Table 3-9 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
NM1, NM2a, NM3, NM4, NM5, NM6, NM7, NM8, NM9, NM10	When one or more documented complaints are received	75 dB(A) ^{Note 1 & Note 2}

Note 1: Acceptable Noise Levels for school should be reduced to 70 dB(A) and 65 dB(A) during examination period.

Note 2: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the NCA have to be followed.

Table 3-10 Action and Limit Levels for Water Quality

Parameter	Performance criteria	Monitoring Location				
		WM1	WM2A(a)	WM2B	WM3x	WM4
DO (mg/L)	Action Level	(*)4.23	(**)4.00	(*)4.74	(**)4.00	(*)4.14
	Limit Level	(#)4.19	(**)4.00	(#)4.60	(**)4.00	(#)4.08
Turbidity (NTU)	Action Level	51.3	24.9	11.4	13.4	35.2
		AND 120% of upstream control station of the same day				
	Limit Level	67.6	33.8	12.3	14.0	38.4
SS (mg/L)	Action Level	54.5	14.6	11.8	12.6	39.4
		AND 120% of upstream control station of the same day				
	Limit Level	64.9	17.3	12.4	12.9	45.5
		AND 130% of upstream control station of the same day				

Remarks:

(*) The Proposed **Action Level** of Dissolved Oxygen is adopted to be used 5%-ile of baseline data

(**) The Proposed **Action & Limit Level** of Dissolved Oxygen is used 4mg/L

(#) The Proposed **Limit Level** of Dissolved Oxygen is adopted to be used 1%-ile of baseline data

3.8.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in **Appendix G**.

3.9 DATA MANAGEMENT AND DATA QA/QC CONTROL

3.9.1 All monitoring data will be handled by the ET's in-house data recording and management system. The monitoring data recorded in the equipment will be downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data will input into a computerized database maintained by the ET. The laboratory results will be input directly into the computerized database and checked by personnel other than those who input the data.

3.9.2 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4 AIR QUALITY MONITORING

4.1 GENERAL

4.1.1 In the Reporting Period, construction works under the project have been commenced in Contracts 2, 3, 4, 6, 7 and Contract SS C505. Hence, air quality monitoring was performed at all designated locations.

4.1.2 The air quality monitoring schedule is presented in *Appendix H* and the monitoring results are summarized in the following sub-sections.

4.2 AIR QUALITY MONITORING RESULTS

4.2.1 In the Reporting Period, a total of *135* events of 1-hour TSP and *50* events 24-hours TSP monitoring were carried out and the monitoring results are summarized in *Tables 4-1 to 4-9*. The detailed 24-hour TSP monitoring data are presented in *Appendix I* and the relevant graphical plots are shown in *Appendix J*.

Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results – AM1c

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
3-Sep-18	34	5-Sep-18	9:42	47	52	57
8-Sep-18	58	11-Sep-18	9:40	70	79	87
14-Sep-18	49	18-Sep-18#	9:34	34	39	41
20-Sep-18	141	22-Sep-18	13:05	61	54	55
26-Sep-18	20	28-Sep-18	9:42	79	83	90
Average (Range)	60 (20-141)	Average (Range)		62 (34 – 90)		

(#) Since the access road to 1-hour TSP monitoring locations AM1c, AM2 & AM3 were blocked by fallen trees due to Typhoon Mangkhut, the monitoring event in these locations scheduled on 17 Sep 18 was cancelled and rescheduled to 18 Sep 18.

Table 4-2 Summary of 24-hour and 1-hour TSP Monitoring Results – AM2

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
3-Sep-18	45	5-Sep-18	9:26	50	57	63
8-Sep-18	106	11-Sep-18	9:25	76	83	90
14-Sep-18	140	18-Sep-18#	9:29	36	41	43
20-Sep-18	117	22-Sep-18	9:30	86	82	77
26-Sep-18	76	28-Sep-18	9:31	85	89	93
Average (Range)	97 (45 – 140)	Average (Range)		70 (36 – 93)		

(#) Since the access road to 1-hour TSP monitoring locations AM1c, AM2 & AM3 were blocked by fallen trees due to Typhoon Mangkhut, the monitoring event in these locations scheduled on 17 Sep 18 was cancelled and rescheduled to 18 Sep 18.

Table 4-3 Summary of 24-hour and 1-hour TSP Monitoring Results – AM3

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
3-Sep-18	59	5-Sep-18	9:23	54	58	65
8-Sep-18	142	11-Sep-18	9:22	72	85	93
14-Sep-18	110	18-Sep-18#	9:25	38	40	44

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
20-Sep-18	25	22-Sep-18	9:17	74	69	60
26-Sep-18	22	28-Sep-18	9:24	80	86	94
Average (Range)	72 (22 – 142)	Average (Range)		67 (38 – 94)		

(#) Since the access road to 1-hour TSP monitoring locations AM1c, AM2 & AM3 were blocked by fallen trees due to Typhoon Mangkhut, the monitoring event in these locations scheduled on 17 Sep 18 was cancelled and rescheduled to 18 Sep 18.

Table 4-4 Summary of 24-hour and 1-hour TSP Monitoring Results – AM4b

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-18	29	3-Sep-18	9:47	50	51	52
7-Sep-18	63	8-Sep-18	9:07	76	78	79
13-Sep-18	27	14-Sep-18	9:20	74	75	71
19-Sep-18	68	20-Sep-18	9:39	51	56	67
24-Sep-18	43	26-Sep-18	13:01	66	72	61
29-Sep-18	108	--	--	--	--	--
Average (Range)	56 (27 – 108)	Average (Range)		65 (50 – 79)		

Table 4-5 Summary of 24-hour and 1-hour TSP Monitoring Results – AM5a

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-18	26	3-Sep-18	9:53	51	49	52
7-Sep-18	45	8-Sep-18	9:10	71	64	69
13-Sep-18	46	14-Sep-18	9:23	77	80	76
19-Sep-18	54	20-Sep-18	9:37	63	75	76
24-Sep-18	38	26-Sep-18	13:14	69	64	73
29-Sep-18	134	--	--	--	--	--
Average (Range)	57 (26 – 134)	Average (Range)		67 (49 – 80)		

Table 4-6 Summary of 24-hour and 1-hour TSP Monitoring Results – AM6

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-18	26	3-Sep-18	10:03	50	56	53
7-Sep-18	74	8-Sep-18	9:18	59	57	63
13-Sep-18	71	14-Sep-18	9:30	76	69	67
19-Sep-18	77	20-Sep-18	9:31	61	70	72
24-Sep-18	49	26-Sep-18	13:39	74	64	72
29-Sep-18	125	--	--	--	--	--
Average (Range)	70 (26 – 125)	Average (Range)		64 (50 – 76)		

Table 4-7 Summary of 24-hour and 1-hour TSP Monitoring Results – AM7b

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-18	24	3-Sep-18	9:17	26	27	28
7-Sep-18	57	8-Sep-18	9:21	43	46	43
13-Sep-18	54	14-Sep-18	9:24	47	54	55
19-Sep-18	89	20-Sep-18	9:45	73	70	68
24-Sep-18	36	26-Sep-18	9:15	78	80	74
29-Sep-18	111	--	--	--	--	--
Average (Range)	62 (24 – 111)	Average (Range)		54 (26 – 80)		

Table 4-8 Summary of 24-hour and 1-hour TSP Monitoring Results – AM8

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-18	21	3-Sep-18	13:13	47	49	49
7-Sep-18	36	8-Sep-18	13:32	48	46	45
13-Sep-18	22	14-Sep-18	13:07	45	44	40
19-Sep-18	108	20-Sep-18	13:07	52	49	48
24-Sep-18	23	26-Sep-18	13:31	74	78	72
29-Sep-18	66	--	--	--	--	--
Average (Range)	46 (21 – 108)	Average (Range)		52 (40 – 78)		

Table 4-9 Summary of 24-hour and 1-hour TSP Monitoring Results – AM9b

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
3-Sep-18	26	5-Sep-18	9:23	53	55	51
8-Sep-18	51	11-Sep-18	9:37	48	50	46
14-Sep-18	44	17-Sep-18	13:31	60	62	59
20-Sep-18	46	22-Sep-18	8:44	86	81	84
26-Sep-18	48	28-Sep-18	9:22	64	70	68
Average (Range)	43 (26 – 51)	Average (Range)		62 (46 – 86)		

4.2.2 As shown in *Tables 4-1 to 4-9*, all the 1-hour TSP and 24-hour TSP monitoring results were below the Action/Limit Levels. No Notification of Exceedance (NOE) was issued in this Reporting Period.

4.2.3 The meteorological data during the impact monitoring days are summarized in *Appendix K*.

5 CONSTRUCTION NOISE MONITORING

5.1 GENERAL

- 5.1.1 In the Reporting Period, construction works under the project have been commenced in Contracts 2, 3, 4, 6, 7 and Contract SS C505 and noise monitoring was performed at all designated locations.
- 5.1.2 The noise monitoring schedule is presented in *Appendix H* and the monitoring results are summarized in the following sub-sections.

5.2 NOISE MONITORING RESULTS

- 5.2.1 In the Reporting Period, a total of **40** events noise measurements were carried out at the designated locations. The sound level meter was set in 1m from the exterior of the building façade including noise monitoring locations NM1, NM3, NM4, NM5, NM6, NM7, NM8 and NM9. Therefore, no façade correction (+3 dB(A)) is added according to acoustical principles and EPD guidelines. However, free-field status were performed at NM2a and NM10 and façade correction (+3 dB(A)) has added according to the requirement in this month. The noise monitoring results at the designated locations are summarized in *Tables 5-1 and 5-2*. The detailed noise monitoring data are presented in *Appendix I* and the relevant graphical plots are shown in *Appendix J*.

Table 5-1 Summary of Construction Noise Monitoring Results

Construction Noise Level ($L_{eq30min}$), dB(A)					
Date	NM1	NM2a ^(*)	NM8	NM9	NM10 ^(*)
5-Sep-18	60	70	60	61	65
11-Sep-18	58	68	56	59	64
17-Sep-18	--	--	63	55	62
18-Sep-18#	54	69	--	--	--
28-Sep-18	56	69	56	58	61
Limit Level	75 dB(A)				

Remarks

- (*) *façade correction (+3 dB(A)) is added according to acoustical principles and EPD guidelines*
- (#) *Since the access road to noise monitoring locations NM1 and NM2a were blocked by fallen trees due to Typhoon Mangkhut, the monitoring event in these locations scheduled on 17 Sep 18 was cancelled and rescheduled to 18 Sep 18.*

Table 5-2 Summary of Construction Noise Monitoring Results

Construction Noise Level ($L_{eq30min}$), dB(A)					
Date	NM3	NM4	NM5	NM6	NM7
3-Sep-18	57	57	59	61	63
14-Sep-18	63	62	55	58	64
20-Sep-18	59	62	57	58	63
26-Sep-18	58	58	56	58	66
Limit Level	75 dB(A)				

- 5.2.2 As shown in *Tables 5-1 and 5-2*, no construction noise measurement results that exceeded the Limit Level were recorded. Moreover, no valid noise complaint (which triggered Action Level exceedance) was recorded in the Reporting Period.

6 WATER QUALITY MONITORING

6.1 GENERAL

6.1.1 In the Reporting Period, construction works under the project has been commenced in Contracts 2, 3, 4, 6, 7 and Contract SS C505 and water quality monitoring was performed at all designated locations. The water quality monitoring schedule is presented in *Appendix H*. The monitoring results are summarized in the following sub-sections.

6.2 RESULTS OF WATER QUALITY MONITORING

6.2.1 In the Reporting Period, a total of **thirteen (13)** sampling days was scheduled to carry out for all designated locations with their control stations. Since exceedances was recorded at WM2A(a), according to “*Event and Action Plan*” stipulation, **4** additional water quality monitoring day was conducted for WM2A(a) and its control stations.

6.2.2 The key monitoring parameters including Dissolved Oxygen, Turbidity and Suspended Solids are summarized in *Tables 6-1 to 6-5*. Breaches of water quality monitoring criteria are shown in *Table 6-6*. Detailed monitoring database including in-situ measurements and laboratory analysis data are shown in *Appendix I* and the relevant graphical plot are shown in *Appendix J*.

Table 6-1 Water Quality Monitoring Results Associated of Contracts 2 and 3

Date	Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
	WM4	WM4-CA	WM4-CB	WM4	WM4-CA	WM4-CB	WM4	WM4-CA	WM4-CB
1-Sep-18	7.5	8.0	7.4	244.5	287.0	219.5	188.5	163.5	153.0
3-Sep-18	7.3	9.6	7.2	595.0	over range	281.5	564.5	744.0	177.0
5-Sep-18	5.3	5.2	5.7	20.4	6.6	9.3	12.5	3.0	8.0
7-Sep-18	7.7	7.6	7.5	16.9	3.9	8.4	16.0	5.5	2.5
11-Sep-18	7.6	7.5	7.2	14.5	4.8	13.8	12.5	2.5	11.5
13-Sep-18	8.2	8.3	8.9	28.7	5.1	15.5	27.5	4.0	12.0
15-Sep-18	7.5	7.3	7.4	16.3	2.7	4.1	23.5	5.5	12.5
18-Sep-18	7.5	7.2	8.0	20.0	3.8	13.7	19.0	<2	7.5
20-Sep-20	7.3	7.3	7.8	23.9	3.0	14.0	24.0	2.5	14.0
22-Sep-20	8.8	8.0	8.5	23.3	7.9	10.5	15.5	2.0	6.0
24-Sep-18	8.0	8.5	7.8	215.0	187.0	134.0	158.0	141.0	101.0
27-Sep-18	7.1	7.8	6.7	12.7	3.0	6.8	9.5	<2	6.0
29-Sep-18	7.1	7.3	6.6	13.7	7.8	22.1	10.5	8.5	23.0

Table 6-2 Water Quality Monitoring Results Associated of Contracts 6 and SS C505

Date	Dissolved Oxygen (mg/L)		Turbidity (NTU)		Suspended Solids (mg/L)	
	WM1	WM1-C	WM1	WM1-C	WM1	WM1-C
1-Sep-18	7.7	7.5	50.7	45.9	50.5	43.5
3-Sep-18	7.8	7.5	29.7	33.2	22.0	34.5
5-Sep-18	6.2	6.4	17.9	16.8	19.5	11.5
7-Sep-18	6.5	6.6	14.4	12.4	13.0	7.0
11-Sep-18	7.8	7.9	17.5	13.7	11.0	6.0
13-Sep-18	7.1	6.5	41.7	11.3	49.5	9.0
15-Sep-18	7.0	6.2	16.6	9.8	50.0	9.0
18-Sep-18	7.3	6.8	17.4	17.0	21.5	5.5
20-Sep-20	6.9	6.9	12.6	13.0	11.0	10.0
22-Sep-18	8.3	7.4	12.7	10.8	12.5	7.5
24-Sep-18	7.6	6.9	11.8	10.8	9.5	7.0
27-Sep-18	5.5	7.0	20.4	15.4	13.0	9.5
29-Sep-18	6.2	7.3	16.8	15.5	13.0	16.5

Table 6-3 Water Quality Monitoring Results Associated only Contract 6

Date	Dissolved Oxygen (mg/L)				Turbidity (NTU)				Suspended Solids (mg/L)			
	WM2A(a)	WM2A-Cx	WM2B	WM2B-C	WM2A(a)	WM2A-Cx	WM2B	WM2B-C	WM2A(a)	WM2A-Cx	WM2B	WM2B-C
1-Sep-18	7.9	8.1	*	*	358.0	364.5	*	*	267.0	334.5	*	*
3-Sep-18	7.3	7.9	*	*	62.9	21.8	*	*	65.0	6.0	*	*
4-Sep-18#	#	#	*	*	11.9	5.2	*	*	10.0	7.0	*	*
5-Sep-18	5.4	5.7	*	*	22.2	11.4	*	*	16.0	4.0	*	*
7-Sep-18	6.8	7.0	*	*	24.1	7.3	*	*	19.0	<2	*	*
11-Sep-18	7.0	6.6	*	*	21.8	11.2	*	*	14.0	2.0	*	*
13-Sep-18	7.1	6.5	*	*	9.2	11.0	*	*	4.0	4.0	*	*
15-Sep-18	6.7	7.0	*	*	12.6	10.5	*	*	8.0	2.0	*	*
18-Sep-18	7.1	6.7	*	*	33.5	9.9	*	*	27.5	<2	*	*
20-Sep-18	6.2	6.4	*	*	12.6	4.9	*	*	10.5	3.0	*	*
21-Sep-18#	#	#	*	*	7.0	3.9	*	*	4.0	<2	*	*
22-Sep-18	6.4	6.8	*	*	17.8	6.2	*	*	14.5	<2	*	*
24-Sep-18	6.8	6.7	*	*	128.5	10.2	*	*	131.5	9.0	*	*
26-Sep-18#	#	#	*	*	15.6	5.8	*	*	14.0	7.0	*	*
27-Sep-18	6.9	7.7	*	*	82.9	6.1	*	*	88.0	2.5	*	*
28-Sep-18#	#	#	*	*	17.8	5.6	*	*	12.0	4.0	*	*
29-Sep-18	6.8	7.5	*	*	15.4	5.0	*	*	14.0	<2	*	*

Remarks: * water sampling was unable to carry out at WM2B and WM2B-C due to shallow water (water depth under 150mm)

Bold and underline indicated Limit Level exceedance

Bold and italic indicated Action Level exceedance

(#) Additional water quality monitoring at the exceeded location(s) due to two consecutive monitoring days indicated Limit Level exceedance

Table 6-4 Water Quality Monitoring Results Associated Contracts 2 and 6

Date	Dissolved Oxygen (mg/L)		Turbidity (NTU)		Suspended Solids (mg/L)	
	WM3x	WM3-C	WM3x	WM3-C	WM3x	WM3-C
1-Sep-18	7.2	7.3	351.5	over range	245.5	672.0
3-Sep-18	6.6	7.3	20.3	99.3	17.0	98.5
5-Sep-18	6.2	6.0	13.3	12.6	17.0	22.5
7-Sep-18	6.2	6.9	6.0	11.5	<2	21.5
11-Sep-18	7.0	7.6	4.4	21.6	3.0	38.5
13-Sep-18	7.8	7.4	13.2	3.5	10.0	6.5
15-Sep-18	7.9	7.2	11.1	7.4	7.0	5.5
18-Sep-18	7.8	7.8	19.0	16.5	24.5	62.5
20-Sep-20	6.8	6.9	11.9	3.6	12.5	9.0
22-Sep-20	7.8	7.3	10.5	38.4	3.5	100.5
24-Sep-18	7.9	7.5	171.0	145.0	263.5	243.0
27-Sep-18	9.0	6.9	7.1	2.6	5.5	5.5
29-Sep-18	6.5	6.8	13.4	2.7	10.0	<2

Table 6-5 Action and Limit (A/L) Levels Exceedance Recorded

Location	Dissolved Oxygen		Turbidity		Suspended Solids		Total Exceedance		Project Related exceedance	
	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
WM1	0	0	0	0	0	0	0	0	0	0
WM2A(a)	0	0	1	3	1	5	2	8	#	#
WM2B	0	0	0	0	0	0	0	0	0	0
WM3x	0	0	0	0	0	0	0	0	0	0
WM4	0	0	0	0	0	0	0	0	0	0
No of Exceedance	0	0	1	3	1	5	2	8	0	0

The exceedances recorded at WM2A(a) on 24 and 27 September are still underway by ET.

6.2.3 In this Reporting Period, a total of ten (10) Action Level/Limit Level exceedances, namely one (1) Action Level and three (3) Limit Level exceedances of turbidity and one (1) Action Level and five (5) Limit Level exceedances of Suspended Solids were recorded for the Project and they are summarized in Table 6-5. Investigation Reports for water quality exceedances have been conducted by ET accordingly. Investigation report revealed that the exceedances recorded at WM2A(a) on 3, 5, 7 and 18 September 2018 were not caused by the works under the Project. Furthermore, the investigation for exceedances recorded at WM2A(a) on 24 and 27 September 2018 are still underway by ET and the investigation result will be presented in next Monthly EM&A Report.

6.2.4 NOE was issued to relevant parties upon confirmation of the monitoring result. The investigation results and summary of exceedances are summarized in **Table 6-6**. The details of the completed investigation reports for the exceedances are attached in **Appendix N**.

Table 6-6 Summary of Water Quality Exceedance in the Reporting Period

Date of Exceedance	Location	Exceeded Parameter	Cause of Water Quality Exceedance In Brief
30 August 2018(last Reporting Period)	WM1	Turbidity & SS	In our investigation, water quality mitigation implemented for Bridge Y and no adverse water quality impact contributed to WM1 was observed. Since muddy water was also observed at control station after rain, it was considered that exceedances were related to the impact of rainstorm and not due to the works under Contract 6.
22, 23 and 24 August 2018(last Reporting Period)	WM2A(a)	Turbidity & SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 22, 23 and 24 August 2018 were related to the impact of rainstorm and not caused by the works under the Project.
27 and 28 August 2018(last Reporting Period)	WM2A(a)	Turbidity & SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 27 and 28 August 2018 were related to the impact of rainstorm and not caused by the works under the Project.

29, 30 and 31 August 2018 (last Reporting Period)	WM2A(a)	Turbidity & SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 29 to 31 August 2018 were related to the impact of rainstorm and not caused by the works under the Project.
3 September 2018	WM2A(a)	Turbidity & SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 3 September 2018 were related to the impact of rainstorm and not caused by the works under the Project.
5 and 7 September 2018	WM2A(a)	SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 5 and 7 September 2018 were not caused by the works under the Project.
18 September 2018	WM2A(a)	Turbidity & SS	In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 18 September 2018 were not caused by the works under the Project.
24 and 27 September 2018	WM2A(a)	Turbidity & SS	The investigation is underway by ET and the investigation findings will be presented in next Reporting Period.

7 ECOLOGY MONITORING

7.1 GENERAL

- 7.1.1 Ecology monitoring for woodland compensation shall be conducted at bi-monthly interval for the first year and the monitoring frequency would be reduced to quarterly from the second year.
- 7.1.2 The Ecology Monitoring for period of June to August 2018 was carried out on 3rd and 6th August 2018 by transects inspection and quadrat monitoring. The Quarterly Ecological Monitoring Report (June to August 2018) which verified by IEC has submitted to EPD as supplementary of the EM&A Report (August 2018) in September 2018. Besides, ecology monitoring is not required in the Reporting Period.

8 WASTE MANAGEMENT

8.1 GENERAL WASTE MANAGEMENT

8.1.1 Waste management was carried out in accordance with the Waste Management Plan (WMP) for each contract.

8.2 RECORDS OF WASTE QUANTITIES

8.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

8.2.2 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 8-1* and *8-2* and the Monthly Summary Waste Flow Table is shown in *Appendix L*. Whenever possible, materials were reused on-site as far as practicable.

Table 8-1 Summary of Quantities of Inert C&D Materials for the Project

Type of Waste	Contract 2		Contract 3		Contract 4		Contract 6		Contract 7		Contract SS C505		Total Qty.
	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	
C&D Materials (Inert) (in '000m ³)	8.0550	--	1.709	--	0	--	0.997	--	0.041	--	7.849	--	18.651
Reused in this Contract (Inert) (in '000 m ³)	0	--	0.381	--	0	--	0	--	0	--	0.161	--	0.542
Reused in other Contracts/ Projects (Inert) (in '000 m ³)	2.8300	Recycling facility as approved alternative site	0	--	0	--	0.552	NENT	0	--	0	--	3.382
Disposal as Public Fill (Inert) (in '000 m ³)	5.2250	Tuen Mun 38	0.967	Tuen Mun 38	0	--	0.445	Tuen Mun 38	0.041	Tuen Mun 38	7.573	TKO 137	14.251

Table 8-2 Summary of Quantities of C&D Wastes for the Project

Type of Waste	Contract 2		Contract 3		Contract 4		Contract 6		Contract 7		Contract SS C505		Total Quantity
	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	Qty.	Disposal location	
Recycled Metal ('000kg) #	30.7800	Licensed collector	0	-	0	--	0	--	1.1	Licensed collector	153.620	Licensed collector	185.5
Recycled Paper / Cardboard Packing ('000kg) #	0.2200	Licensed collector	0	-	0	-	0.225	Licensed collector	0.1	Licensed collector	0.620	Licensed collector	1.165
Recycled Plastic ('000kg) #	1.8000	Licensed collector	0	-	0	--	0	--	0.001	Licensed collector	0.033	Licensed collector	1.834
Chemical Wastes ('000kg) #	1.2300	Licensed collector	0	-	0	--	0	--	0	--	0	--	1.23
General Refuses ('000m ³)	0.4440	NENT	0.150	NENT	0	--	0.633	NENT	0.1	NENT	2.704	NENT	4.031

Remark #: Unit of recycled metal, recycled paper/ cardboard packing, recycled plastic and chemical waste for Contract 3 was in ('000m³) while the unit of chemical waste for Contract 3 was in (m³).

9 SITE INSPECTION

9.1 REQUIREMENTS

9.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

9.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

Contract 2

9.2.1 In the Reporting Period, joint site inspection for Contract 2 to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 21 and 28 September 2018**. No non-compliance was noted.

9.2.2 The findings / deficiencies of **Contract 2** that observed during the weekly site inspection are listed in **Table 9-1**.

Table 9-1 Site Observations for Contract 2

Date	Findings / Deficiencies	Follow-Up Status
7 September 2018	<ul style="list-style-type: none"> Unsealed hoarding foot and stagnant water was observed at south portal. The Contractor should seal the hoarding foot of the boundary to prevent surface runoff and remove the stagnant water. The Contractor was reminded to update the discharge license if there has any change of treatment methods and discharge points. 	<ul style="list-style-type: none"> The hoarding foot was sealed. Not required for reminder.
14 September 2018	<ul style="list-style-type: none"> Free standing chemical containers were observed at South Portal. The Contractor should provide drip trays for any chemical containers to prevent leakage. The Contractor was reminded to clarify the use of unknown pipe at mid vent. The Contractor was reminded to update the discharge license and the treatment methods for existing discharge point. 	<ul style="list-style-type: none"> The chemical containers were removed. Not required for reminder. Not required for reminder.
21 September 2018	<ul style="list-style-type: none"> Generators without NRMM labels were observed at North Portal. The Contractor should provide NRMM labels for generators used in site. 	<ul style="list-style-type: none"> The NRMM labels were provided.
28 September 2018	<ul style="list-style-type: none"> Water appear to be turbid was observed at south portal of discharge point. The contractor should properly treated the wastewater before discharge 	<ul style="list-style-type: none"> To be followed up.

Contract 3

9.2.3 In the Reporting Period, joint site inspection for Contract 3 to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **6, 13, 19 and 27 September 2018**. No non-compliance was noted.

9.2.4 The findings / deficiencies of **Contract 3** that observed during the weekly site inspection are listed in **Table 9-2**.

Table 9-2 Site Observations for Contract 3

Date	Findings / Deficiencies	Follow-Up Status
6 September	<ul style="list-style-type: none"> Silty discharge was observed at WWTS-1. 	<ul style="list-style-type: none"> The pipe was

Date	Findings / Deficiencies	Follow-Up Status
2018	The Contractor should provide proper mitigation measure to ensure all waste water was treated prior to discharge. <ul style="list-style-type: none"> • The Contractor was reminded to maintain WWTS-13 in proper operation. 	removed. <ul style="list-style-type: none"> • Not required for reminder.
13 September 2018	<ul style="list-style-type: none"> • Muddy trails and muddy water were observed at public road (Site exit SA13 and SA 2). The Contractor should clean the muddy trails, wash the wheels thoroughly before leaving the site and provide measures to divert the wheel washing waste water for treatment and ensure no muddy trail present at the public road. 	<ul style="list-style-type: none"> • Muddy rails and muddy water at public road was clean. Last observation closed.
19 September 2018	<ul style="list-style-type: none"> • Overflow of muddy water from wheel washing to public road was observed at work area of site exit SA2. The Contractor was advised to clean the muddy water as soon as possible and provide proper mitigation to avoid muddy water flow out of site. • The Contractor was reminded to maintain all the site entrance in good condition. 	<ul style="list-style-type: none"> • Muddy water at public road was clean. Last observation closed. • Not required for reminder.
27 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA

Contract 4

9.2.5 In the Reporting Period, joint site inspection for Contract 4 to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 21 and 24 September 2018**. No non-compliance was noted.

9.2.6 The findings / deficiencies of **Contract 4** that observed during the weekly site inspection are listed in **Table 9-3**.

Table 9-3 Site Observations for Contract 4

Date	Findings / Deficiencies	Follow-Up Status
7 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA
14 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA
21 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA
24 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA

Contract 6

9.2.7 In the Reporting Period, joint site inspection for Contract 6 to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **6, 13, 20 and 27 September 2018**. No non-compliance was noted.

9.2.8 The findings / deficiencies of **Contract 6** that observed during the weekly site inspection are listed in **Table 9-4**.

Table 9-4 Site Observations for Contract 6

Date	Findings / Deficiencies	Follow-Up Status
6 September 2018	<ul style="list-style-type: none"> The Contractors was reminded to remove the silt and maintain the temporary drainage system at Chuk Yuen village. Muddy water was observed on the pedestrian and sand was observed along the water gilled barriers under bridge Y. The Contractor has arranged cleaning and silt removing. It will follow up on next weekly site inspection, 	<ul style="list-style-type: none"> Not required for reminder. No muddy water was observed on the pedestrian.
13 September 2018	<ul style="list-style-type: none"> The Contractor was reminded to provide sandbags, cover stockpiles and open slope with tarpaulin sheets before rainstorm to prevent muddy runoff. The Contractor was reminded to wash the wheel before leaving the site and maintain the site exit clean and tidy. The Contractor was reminded to maintain waste water treatment facility in function at North Portal. 	<ul style="list-style-type: none"> Not required for reminder. Not required for reminder. Not required for reminder.
20 September 2018	<ul style="list-style-type: none"> Muddy runoff was observed at bridge Y. The Contractor should provide proper mitigation measures to ensure no muddy water seepage from the site. 	<ul style="list-style-type: none"> Sand bags bunding has been provided to prevent the seepage of muddy water.
27 September 2018	<ul style="list-style-type: none"> No adverse environmental issue was observed. 	<ul style="list-style-type: none"> NA

Contract SS C505

9.2.9 In the Reporting Period, joint site inspection for Contract SS C505 to evaluate the site environmental performance has been carried out by the RE, ET and the Contractor on **5, 12, 19 and 27 September 2018** in which IEC joined the site inspection on **27 September 2018**. No non-compliance was noted.

9.2.10 The findings / deficiencies of **Contract SS C505** that observed during the weekly site inspection are listed in **Table 9-5**.

Table 9-5 Site Observations for Contract SS C505

Date	Findings / Deficiencies	Follow-Up Status
5 September 2018	<ul style="list-style-type: none"> Stagnant water was observed near building 1. The Contractor should provide proper mitigation measure to prevent mosquito breeding. 	<ul style="list-style-type: none"> Construction materials was covered by tarpaulin sheets.
12 September 2018	<ul style="list-style-type: none"> The construction was reminded to remove stagnant water regularly. 	<ul style="list-style-type: none"> Not required for reminder.
19 September 2018	<ul style="list-style-type: none"> The construction was reminded to remove construction waste and general waste regularly. 	<ul style="list-style-type: none"> Not required for reminder.
27 September 2018	<ul style="list-style-type: none"> Two unknown chemical containers were observed on the ground of 1st floor of PTB. The contractor should check whether they are chemical wastes, if yes they should properly handle and place chemical containers inside drip tray to avoid leakage and provide with proper labelling. Cement grouting activity without proper 	<ul style="list-style-type: none"> To be followed up. To be followed up.

Date	Findings / Deficiencies	Follow-Up Status
	shelter area was observed at 1st floor of PTB. The Contractor should provide shelter area with three-side and top for cement grouting activity to avoid dust emission.	

Contract 7

9.2.11 In the Reporting Period, joint site inspection for Contract 7 to evaluate the site environmental performance has been carried out by the RE, IEC, ET and the Contractor on **7, 14, 18 and 28 September 2018**. No non-compliance was noted.

9.2.12 The findings / deficiencies of **Contract 7** that observed during the weekly site inspection are listed in **Table 9-6**.

Table 9-6 Site Observations for Contract 7

Date	Findings / Deficiencies	Follow-Up Status
7 September 2018	<ul style="list-style-type: none"> • The Contractor was reminded to remove construction waste and general waste regularly. 	<ul style="list-style-type: none"> • Not required for reminder.
14 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA
18 September 2018	<ul style="list-style-type: none"> • The Contractor was reminded to maintain the sedimentation tanks function properly. • The Contractor was reminded to remove stagnant water regularly. 	<ul style="list-style-type: none"> • Not required for reminder. • Not required for reminder.
28 September 2018	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • NA

9.2.13 General housekeeping such as daily site tidiness and cleanliness should be maintained for all Contracts. Furthermore, the Contractors were reminded to implement Waste Management Plan of the Project.

10 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

10.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTIONS

10.1.1 In the Reporting Period, no environmental complaints were received under the EM&A program of the Project. Moreover, no summons and prosecution under the EM&A Programme was lodged for all Contracts. The status of the outstanding investigation report in previous months is summarized below.

10.1.2 The statistical summary of environmental complaint is presented in *Tables 10-1, 10-2 and 10-3*.

Table 10-1 Statistical Summary of Environmental Complaints

Reporting Period	Contract No	Environmental Complaint Statistics			Project related complaint
		Frequency	Cumulative	Complaint Nature	
19 May 2014 – 31 August 2018	Contract 2	0	35	<ul style="list-style-type: none"> • (19) Water Quality • (8) Dust • (5) Noise • (1) dust & noise • (1) waste management • (1) Water quality and dust 	(7) water quality (2) dust (1) noise
06 Nov 2013 – 31 August 2018	Contract 3	0	6	<ul style="list-style-type: none"> • (2) Dust • (3) Water quality • (1) Noise 	0
16 Aug 2013 – 31 August 2018	Contract 5	0	4	<ul style="list-style-type: none"> • (3) Dust • (1) Noise 	0
16 Aug 2013 – 31 August 2018	Contract 6	0	39	<ul style="list-style-type: none"> • (24) Water Quality • (8) Dust • (3) Noise • (1) Nuisance • (1) Noise and dust • (2) Water quality and dust 	(8) water quality (3) dust (1) Nuisance (1) Water quality and dust
15 Feb 2016 – 31 August 2018	Contract 7	0	3	<ul style="list-style-type: none"> • (1) Noise • (2) Water quality and dust 	(1) Water quality and dust
16 Aug 2013 – 31 August 2018	SS C505	0	5	<ul style="list-style-type: none"> • (1) Noise • (1) dust • (2) Water quality and dust • (1) Water quality 	(1) Water quality and dust
1 – 30 September 2018	Contract 2	0	35	<ul style="list-style-type: none"> • (19) Water Quality • (8) Dust • (5) Noise • (1) dust & noise • (1) waste management • (1) Water quality and dust 	NA
	Contract 3	0	6	<ul style="list-style-type: none"> • (2) Dust • (3) Water quality • (1) Noise 	NA
	Contract 4	0	0	NA	NA

Reporting Period	Contract No	Environmental Complaint Statistics			Project related complaint
		Frequency	Cumulative	Complaint Nature	
	Contract 6	0	39	<ul style="list-style-type: none"> • (24) Water Quality • (8) Dust • (3) Noise • (1) Nuisance • (1) Noise and dust • (2) Water quality and dust 	NA
	Contract 7	0	3	<ul style="list-style-type: none"> • (1) Noise • (2) Water quality and dust 	NA
	SS C505	0	5	<ul style="list-style-type: none"> • (1) Noise • (1) dust • (2) Water quality and dust • (1) Water quality 	NA

Table 10-2 Statistical Summary of Environmental Summons

Reporting Period	Contract No	Environmental Summons Statistics		
		Frequency	Cumulative	Complaint Nature
19 May 2014 – 31 August 2018	Contract 2	0	1	contravening the Water Pollution Control (General) Regulations
06 Nov 2013 – 31 August 2018	Contract 3	0	0	NA
16 Aug 2013 – 31 August 2018	Contract 5	0	0	NA
16 Aug 2013 – 31 August 2018	Contract 6	0	0	NA
15 Feb 2016 – 31 August 2018	Contract 7	0	0	NA
16 Aug 2013 – 31 August 2018	SS C505	0	0	NA
1 – 30 September 2018	Contract 2	0	1	NA
	Contract 3	0	0	NA
	Contract 4	0	0	NA
	Contract 6	0	0	NA
	Contract 7	0	0	NA
	SS C505	0	0	NA

Table 10-3 Statistical Summary of Environmental Prosecutions

Reporting Period	Contract No	Environmental Prosecutions Statistics		
		Frequency	Cumulative	Complaint Nature
19 May 2014 – 31 August 2018	Contract 2	0	1	contravening the Water Pollution Control (General) Regulations
06 Nov 2013 – 31 August 2018	Contract 3	0	0	NA
16 Aug 2013 – 31 August 2018	Contract 5	0	0	NA
16 Aug 2013 – 31 August 2018	Contract 6	0	0	NA
15 Feb 2016 – 31 August 2018	Contract 7	0	0	NA
16 Aug 2013 – 31 August 2018	SS C505	0	0	NA
1 – 30 September 2018	Contract 2	0	1	NA
	Contract 3	0	0	NA
	Contract 4	0	0	NA

Reporting Period	Contract No	Environmental Prosecutions Statistics		
		Frequency	Cumulative	Complaint Nature
	Contract 6	0	0	NA
	Contract 7	0	0	NA
	SS C505	0	0	NA

11 IMPLEMENTATION STATUS OF MITIGATION MEASURES

11.1 GENERAL REQUIREMENTS

- 11.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in *Appendix M*.
- 11.1.2 All contracts under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented by Contracts 2, 3, 4, 5, 6, 7 and Contract SS C505 in this Reporting Period are summarized in *Table 11-1*.

Table 11-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> Wastewater to be treated by the wastewater treatment facilities i.e. sedimentation tank or similar facility before discharge.
Air Quality	<ul style="list-style-type: none"> Maintain damp / wet surface on access road Low vehicular speed within the works areas. All vehicles must use wheel washing facility before off site Sprayed water during breaking works A cleaning truck was regularly performed on the public road to prevent fugitive dust emission
Noise	<ul style="list-style-type: none"> Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants Place noisy plants away from residence or school Provide noise barriers or hoarding to enclose the noisy plants or works Shut down the plants when not in used.
Waste and Chemical Management	<ul style="list-style-type: none"> On-site sorting prior to disposal Follow requirements and procedures of the “Trip-ticket System” Predict required quantity of concrete accurately Collect the unused fresh concrete at designated locations in the sites for subsequent disposal
General	<ul style="list-style-type: none"> The site was generally kept tidy and clean.

11.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 11.2.1 As advised by the ER, the construction works under Contract 5 was substantially completed on 31 August 2016. Construction activities for other Contracts in the coming month are listed below:

Contract 2

Mid-Vent Portal	<ul style="list-style-type: none"> Building fit out and E&M installation Construction of flexible barrier and permanent drainage Landscaping works.
North Portal	<ul style="list-style-type: none"> Construction of retaining wall, permanent drainage and slip road Tunnel backfilling, VE panel and E&M installation Construction of tunnel internal structure Landscaping works North ventilation building fit out and E&M installation
South Portal	<ul style="list-style-type: none"> Construction of tunnel internal structure, tunnel backfilling and E&M installation South ventilation building fit out and E&M installation Construction of flexible barrier Landscaping works. Backfilling and construction of slip road
Admin Building	<ul style="list-style-type: none"> Building fit out, permanent drainage and E&M installation Landscaping works

Contract 3

- Cable detection and trial trenches
- Remaining works on new Footbridge
- Noise barrier construction
- Road pavement works
- Water main laying works (on Grade and on bridge deck)
- Installation of Noise barrier steel column & panel, and sign gantry (on Grade and on bridge deck)
- Road Drainage Works
- Waterproofing works on bridge deck
- Bitumen paving on bridge deck
- Installation of movement joint on the bridge
- Construction of retaining wall
- Landscaping works

Contract 4

- E&M installation at Admin Building
- E&M installation at Ventilation Building
- E&A installation at OHVD & tunnel
- High mast erection
- Cladding installation at Cheung Shan Tunnel
- Sign fabrication & installation

Contract 6

- Bridge construction
- Tunnel Works
- Sewage Treatment Plant Construction
- Tunnel Ventilation Building Construction
- Slip Road/At-grade Road/Periphery Road Construction

Contract 7

- Profile barrier construction at Bridges A and E
- Noise barrier construction at Bridge D and E
- Parapet installation at Bridge A, B, D and E
- Drainage pipe laying at Bridge A, B, D and E
- Waterproofing and drainage works at Roof of Bridge C
- Drainage and watermains at perimeter road
- Bitumen pavement at perimeter road

Contract SS C505

- Passenger Terminal Building (PTB) G/F - Plant Room Structure Works, Backfilling & Drainage, Under Ground Utilities, Fence Wall and On Grade Slab
- PTB - ABWF Works & MEP Installation - Front/Back of House Area, External Staircases, Hall Block External Façade, Southern Entrance Construction, Major Plant Rooms
- PTB - External Works incl. Building 21-24, M/F External Wall (Ewall), Roof & Upper Roof Roofing Works, Podium Coach Canopy, 21&22 (C&PC KIOSKS) & 23&24 (PC Examination Building & MSRVSS) Superstructure & ABWF Works and MEP Installation, Podium Open Area Waterproofing, Paving, Hard and Soft Landscaping works, Ambulance Canopy / Glazed Canopy
- Bridge C Integrated ABWF and MEP Installation Works (C7 Portion)
- Bldg 1 - C&ED Detector Dog Base Phase 1 - Integrated ABWF & MEP Works Works at G/F & R/F
- Bldg 2 - HKPF Building and Observation Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to 4/F and Observation Tower (including Lift)

- Bldg 3 - Fire Station and Drill Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to UR/F, Drill Tower
- Bldg 4 - Cargo Examination Building (Inbound) Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
- Bldg 5 - Cargo Examination Building (Outbound) Phase 2 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
- Bldg 6 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Inbound) - External Works Fence Wall, Integrated ABWF & MEP Works at G/F to R/F
- Bldg 7 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Outbound) - Integrated ABWF & MEP Works at G/F
- Bldg 8 - MXRVSS (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & R/F
- Bldg 9 - MXRVSS (Outbound) Phase 2 - Structure Works at G/F, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 10 - GV Kiosk (Inbound) Phase 2 - On-Grade Slab, Steel Structure Works, Integrated ABWF and MEP Works at G/F & R/F
- Bldg 11 - GV Kiosk (Outbound) Phase 2 - Steel Structure Works, Integrated ABWF & MEP Works at G/F & R/F
- Bldg 12 - Public Toilets (Inbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 13 - Public Toilets (Outbound) Phase 2 - Structures Works, Integrated ABWF and MEP Works at G/F & R/F
- Bldg 14 - Disinsection Facilities (Inbound) Phase 2 - Integrated ABWF & MEP Works at G/F & Envelope
- Bldg 15 - Disinsection Facilities (Outbound) Phase 2 - Substructure and Structure Works, Integrated ABWF & MEP Works at G/F & Envelope
- Bldg 16 - Weigh Station Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 17 - EUVSS & Monitoring Room Phase 2 - Structure Works, Integrated ABWF & MEP Works at G/F & R/F
- Bldg 18 - Refuse Collection Point Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 25 - Traffic Control Office (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 26 - Traffic Control Office (Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 27 - Inspection Post Phase 2 - Structure Works, Integrated ABWF and MEP Work at G/F & Envelope
- Bldg 28, 30 & 31 - Guard Booth (Inbound/Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
- Bldg 32 to 35 - Steel Canopies Phase 2 - Structure Works, Integrated ABWF and MEP Works
- Bldg 37 to 40 - Elevated Walkway (E1, E2, E3 & E4) Phase 2 - Structures Works, ABWF and BS Works
- Vehicular bridges 1 to 5 Phase 3 - Retaining walls, Road and Finishes Works
- External Works - CLP Cable & Power ON Transfer room
- External Works - Water Meter Room Connection (Inbound & Outbound)
- External Works - External Utilities, UU works & DSD Inspection
- External Works - Road & Pavement Works
- Landscape - Inbound Area
- Testing & Commissioning (T&C) and FSD Inspection - CBO, FXO, Inbound & Outbound Group Buildings

11.3 KEY ISSUES FOR THE COMING MONTH

- 11.3.1 Key issues to be considered in the coming month for Contracts 2, 3, 4, 6, 7 and SS C505 include:
- Implementation of control measures for rainstorm;

- Regular clearance of stagnant water during wet season;
- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Discharge of site effluent to the nearby wetland, stockpiling or disposal of materials, and any dredging or construction area at this area are prohibited;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

12 CONCLUSIONS AND RECOMMENDATIONS

12.1 CONCLUSIONS


- 12.1.1 This is the **62nd** monthly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from **1 to 30 September 2018**.
- 12.1.2 For air quality monitoring, no 1-hour TSP and 24-hour TSP monitoring results triggered the Action or Limit Levels were recorded.
- 12.1.3 In the Reporting Period, no construction noise measurement results that exceeded the Limit Level were recorded. Moreover, no valid noise complaint which triggered an Action Level exceedance was recorded.
- 12.1.4 For water quality monitoring, a total of ten (10) Action Level/Limit Level exceedances, namely one (1) Action Level (3) Limit Level exceedance of turbidity and one (1) Action Level and five (5) Limit Level exceedances of Suspended Solids were recorded for the Project. Investigation report revealed the Contractor had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. It was concluded that the exceedance recorded at WM2A(a) on 3, 5, 7 and 18 September 2018 were not caused by the works under the Project. Furthermore, the investigation for exceedances recorded at WM2A(a) on 24 and 27 September 2018 are still underway by ET and the investigation result will be presented in next Monthly EM&A Report.
- 12.1.5 In this Reporting Period, no environmental complaints, environmental summons and prosecution were received under the EM&A programme.
- 12.1.6 During the Reporting Period, weekly joint site inspection by the RE, IEC, ET with the relevant Main-contractor were carried out for Contracts 2, 3, 4, 6 and 7 in accordance with the EM&A Manual stipulation. For Contract SS C505, weekly joint site inspection was carried out by the RE, IEC, ET and main-contractor whereas IEC performed monthly site inspection. No non-compliance observed during the site inspection.

12.2 RECOMMENDATIONS

- 12.2.1 During rainy season, preventive measures for muddy water or other water pollutants from site surface flow to local stream such as Kong Yiu Channel, Ma Wat Channel, Ping Yuen River, Kwan Tei River or public area should be properly maintained. The Contractors should paid special attention on water quality mitigation measures and fully implement according ISEMM of the EM&A Manual, in particular for working areas near Ma Wat Channel and Ping Yuen River.
- 12.2.2 In addition, all effluent discharge shall be ensure to fulfill Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or discharge permits stipulation.
- 12.2.3 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants should be implemented in accordance with the EM&A requirement.
- 12.2.4 Since most of construction sites under the Project are located adjacent to villages, the Contractors should fully implement air quality mitigation measures to reduce construction dust emission.
- 12.2.5 Furthermore, daily cleaning and weekly tidiness shall be properly performed and maintained. In addition, mosquito control should be kept to prevent mosquito breeding on site.

Appendix A

Layout plan of the Project



LOCATION PLAN
SCALE 1 : 3000

LEGEND:

UNDERGROUND WORKS

DATE	REVISION	BY	CHK	APP

土木工務發展署
CEDD
Civil Engineering and
Development Department

LIANJIAN/HEUNG YUEN WAI BOUNDARY
(SITE FORMATION AND INFRASTRUCTURES)
DESIGN AND CONSTRUCTION

PROJECT LAYOUT PLAN

AECOM



DRGNO. 60212563/PLP/001
圖紙編號

SCALE: 1:3000
比例尺

DATE: 15/10/2015
日期


PROJECT: 60212563/PLP/001
項目名稱

COPYRIGHT RESERVED
版權保留

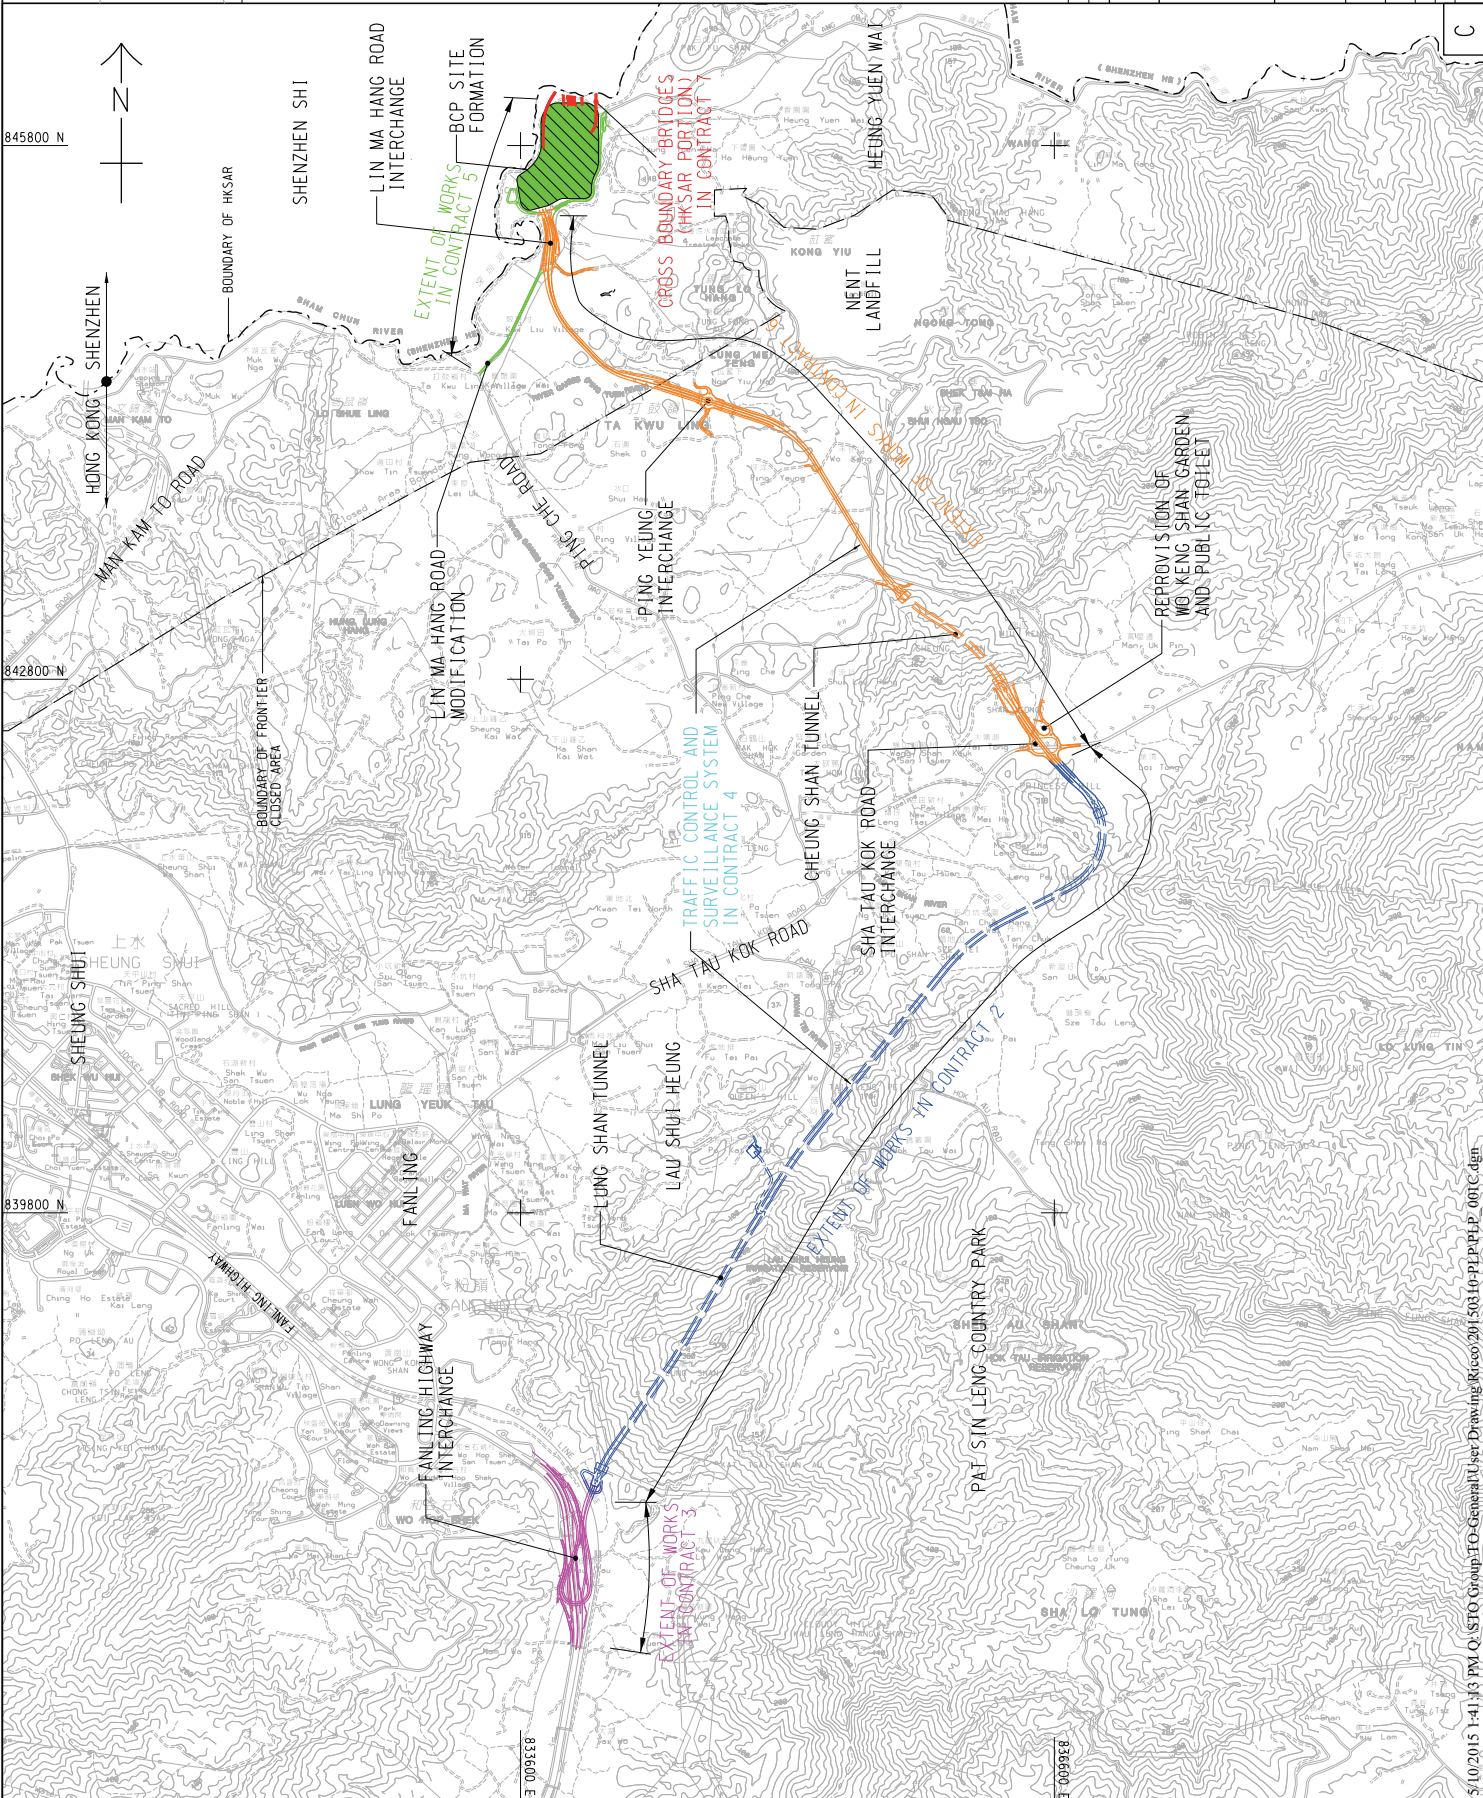

Appendix B

Organization Chart

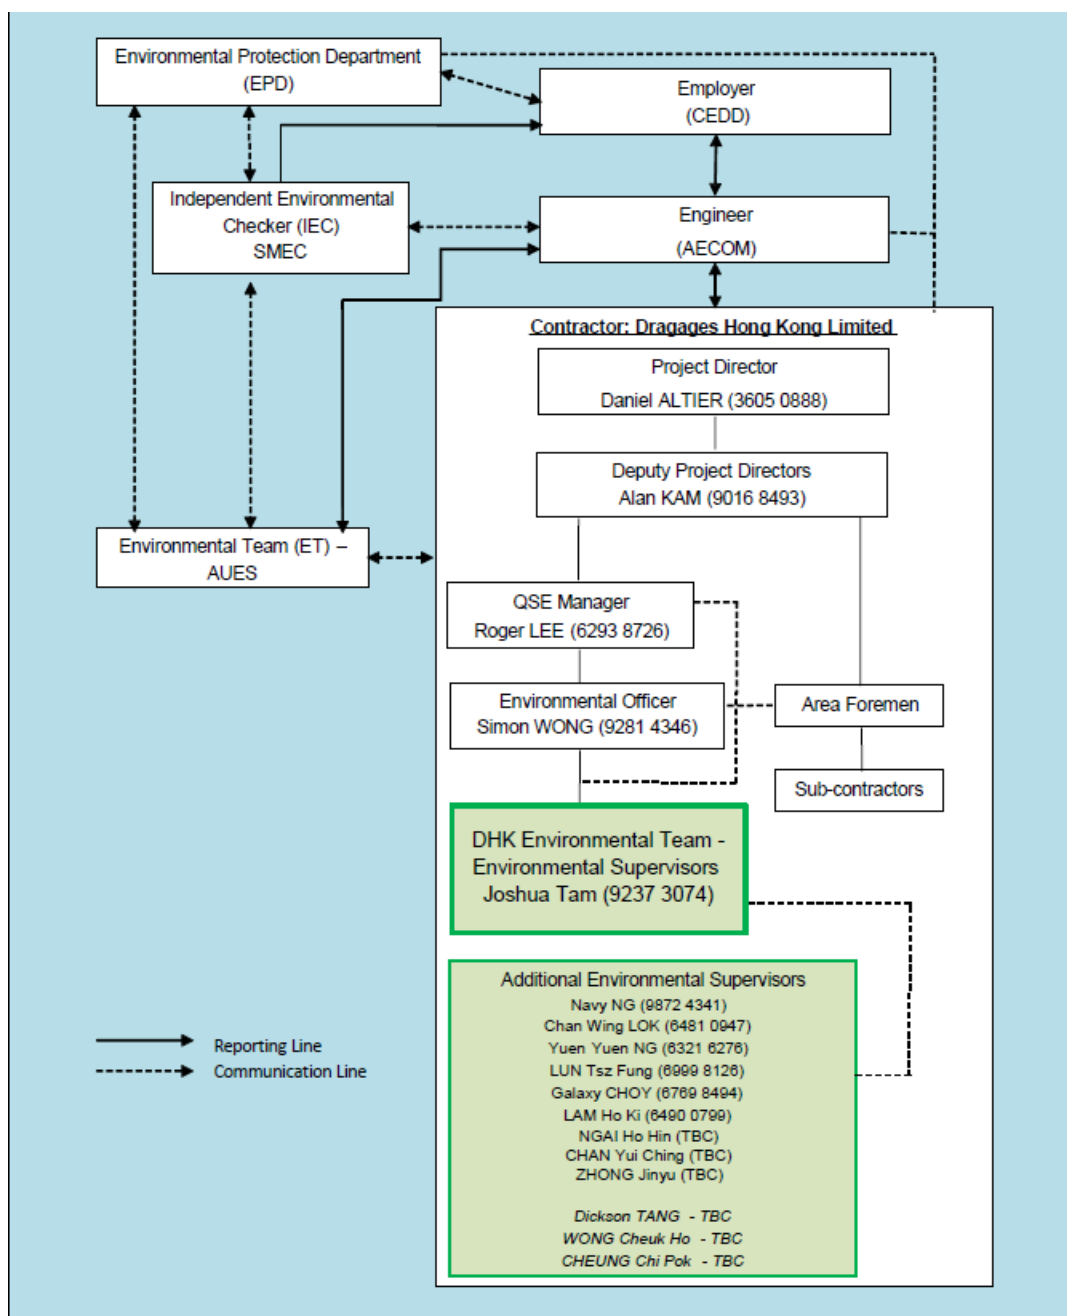

Environmental Management Organization for Contract 2 - (CV/2012/08)

Contact Details of Key Personnel for Contract 2 - CV/2012/08

Organization	Project Role	Name of Key Staff	Tel No	Fax No.
AECOM	Engineer’s Representative	Edwin Ching	2171 3301	2171 3498
SMEC	Independent Environmental Checker	Antony Wong	3995 8120	3995 8101
DHK	Project Director	Daniel Altier	3605 0888	2171 3299
DHK	Deputy Project Manager	Alan Kam	9016 8493	2171 3299
DHK	QSE Manager	Roger Lee	6293 8726	2171 3299
DHK	Environmental Officer	Simon Wong	2171 3017	2171 3299
DHK	Environmental Supervisor	Joshua Tam	9237 3074	2171 3299
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:


CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

DHK(Main Contractor) –Dragages Hong Kong Ltd.

SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

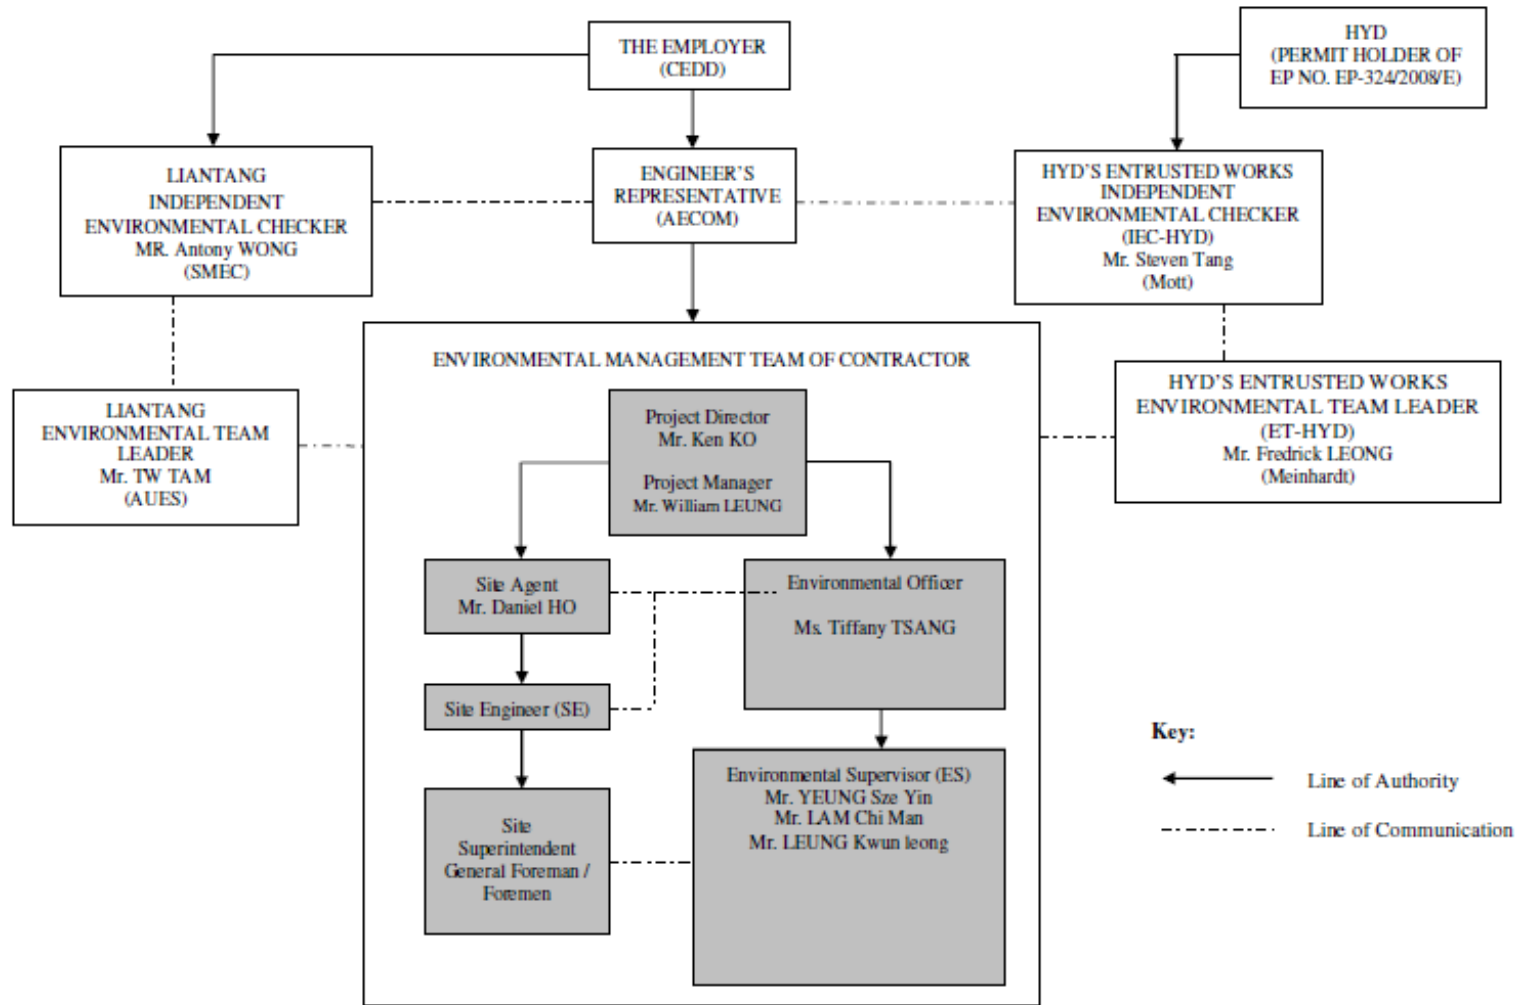

Environmental Management Organization for Contract 3 - CV/2012/09

Contact Details of Key Personnel for Contract 3 - CV/2012/09

Organization	Project Role	Name of Key Staff	Tel No	Fax No.
AECOM	Engineer's Representative	Alan Lee	2171 3303	2171 3498
SMEC	Independent Environmental Checker	Antony Wong	3995 8120	3995 8101
Chun Wo	Project Director	Ken Ko	3758 8735	2638 7077
Chun Wo	Project Manager	William Leung	2638 6136	2638 7077
Chun Wo	Site Agent	Daniel Ho	2638 6144	2638 7077
Chun Wo	Environmental Officer	TBA	2638 6151	2638 7077
Chun Wo	Environmental supervisor	Frankie Leung	2638 6125	2638 7077
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Remark: (#) The key staff for Environmental Officer has left her position on 10 July 2018 and her replacement will be included in next Reporting Month.

Legend:

CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

Chun Wo (Main Contractor) – Chun Wo Construction Ltd.


SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

Contract No. NE/2014/02 (C4)

Site Safety and Environmental Organizational Chart

As of 31 Jul 2018

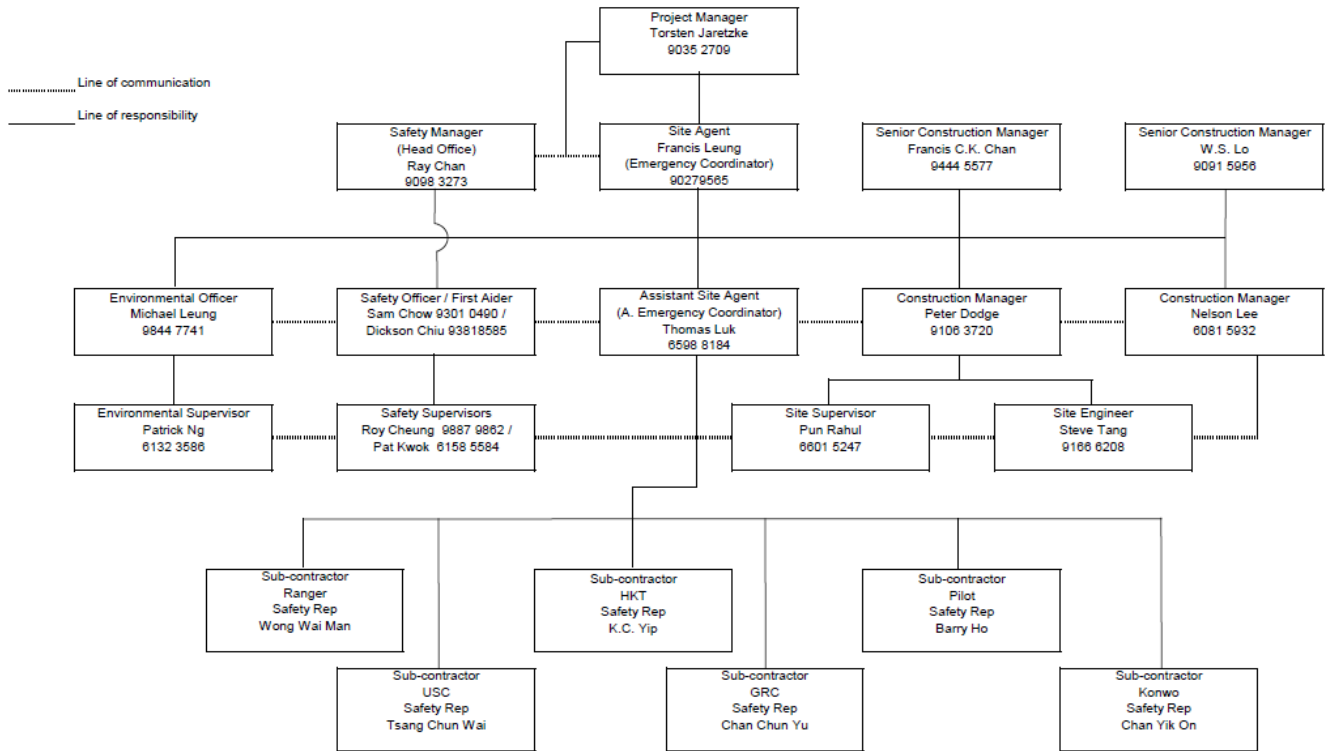

Environmental Management Organization for Contract 4 - NE/2014/02

Contact Details of Key Personnel for Contract 4 - NE/2014/02

Organization	Project Role	Name of Key Staff	Tel No	Fax No.
AECOM	Engineer's Representative	Leo Lai	2171 3310	2171 3498
SMEC	Independent Environmental Checker	Antony Wong	3995 8120	3995 8101
Siemens	Project Manager	Torsetn Jaretzke	9035 2709	--
Siemens	Site Agent	Francis Leung	9027 9565	--
Siemens	Environmental Officer	Michael Leung	9844 7741	--
Siemens	Environmental Supervisors	Eric Lee	9092 3356	--
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:


CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

Siemens (Main Contractor) – Siemens Ltd.

SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

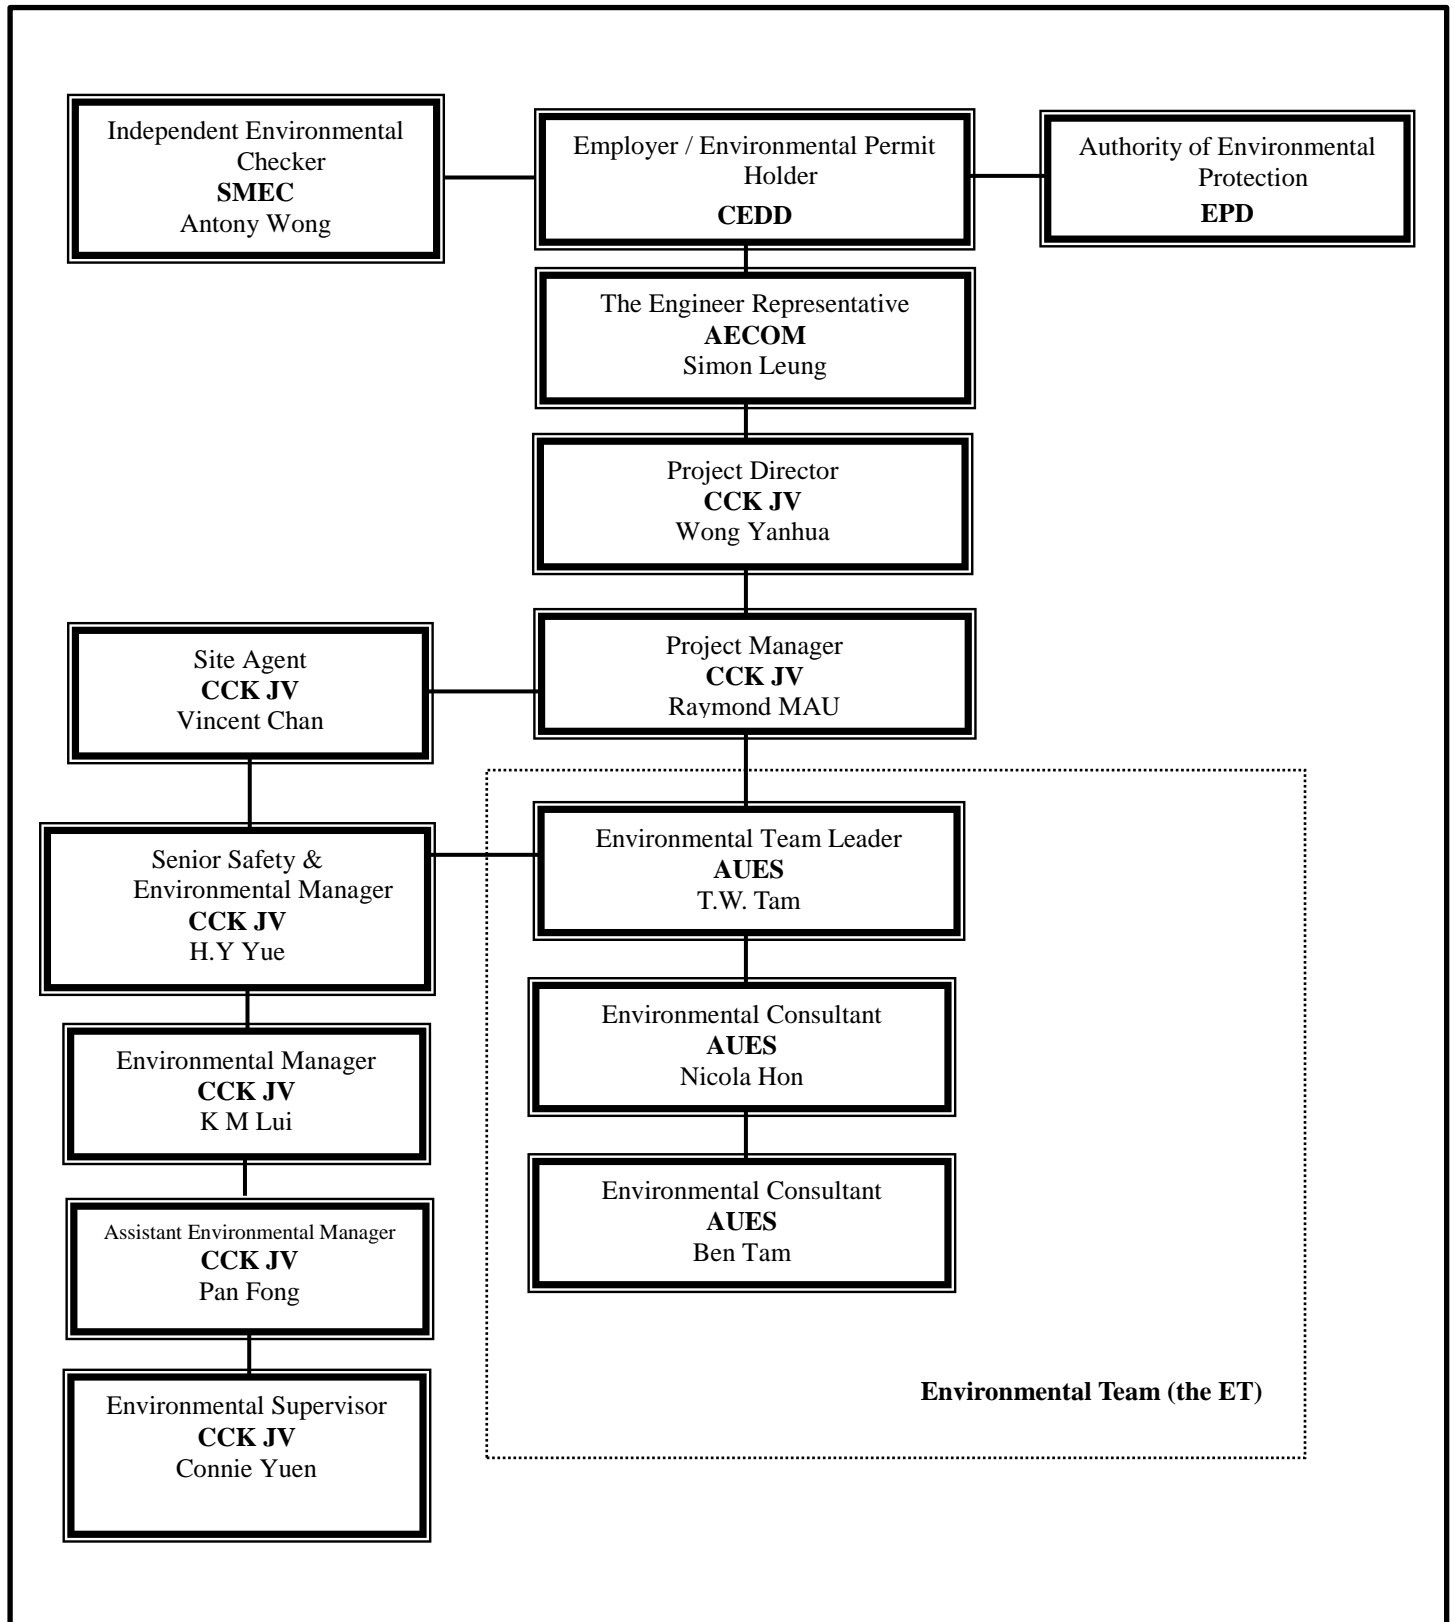

Environmental Management Organization – CV/2013/08

Contact Details of Key Personnel for Contract 6 - CV/2013/08

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
AECOM	Engineer's Representative	Simon Leung	2251 0688	2251 0698
SMEC	Independent Environmental Checker	Antony Wong	3995 8120	3995 8101
CCK JV	Project Director	Wang Yanhua	6190 4212	--
CCK JV	Project Manager	Raymond Mau Sai-Wai	9011 5340	--
CCK JV	Site Agent	Vincent Chan	9655 9404	--
CCK JV	Senior Safety & Environmental Manager	H.Y. Yue	9185 8186	--
CCK JV	Environmental Manager	K M Lui	51138223	--
CCK JV	Assistant Environmental Manager	Pan Fong	9436 9432	--
CCK JV	Environmental Supervisor	Connie Yuen	6316 6931	--
AUES	Environmental Team Leader	TW Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079

Legend:


CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

CCK JV (Main Contractor) – CRBE-CEC-Kaden Joint Venture

SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

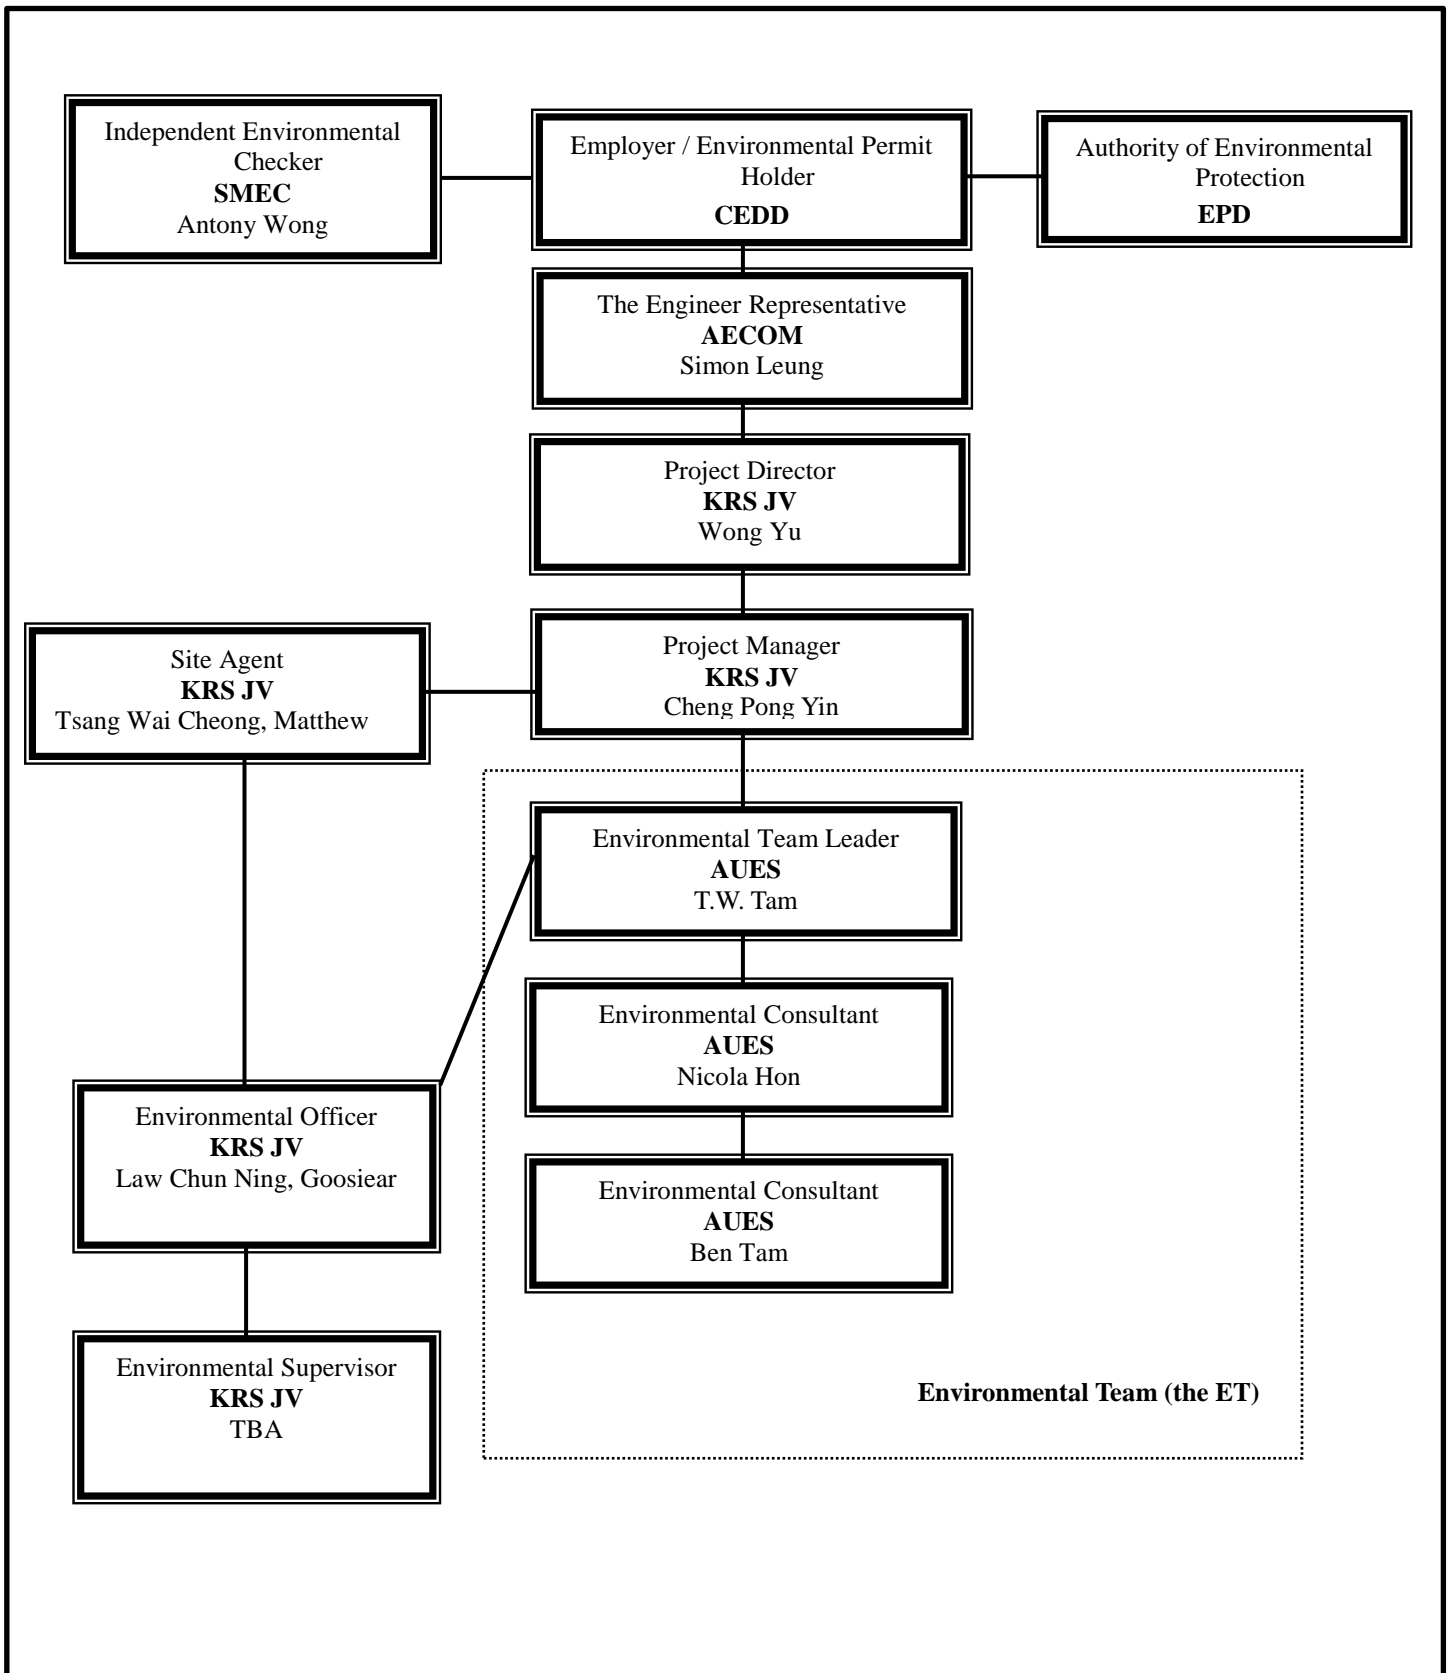

Environmental Management Organization –NE/2014/03

Contact Details of Key Personnel for Contract 7 – NE/2014/03

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
AECOM	Engineer's Representative	Kelvin lee	2251 0609	2251 0698
SMEC	Independent Environmental Checker	Antony Wong	3995 8120	3995 8101
KRSJV	Project Director	Wong Yu	2682 6691	2682 2783
KRSJV	Project Manager	Cheng Pong Yin	9023 4821	2682 2783
KRSJV	Site Agent	Tsang Wai Cheong, Matthew	9705 7536	2682 2783
KRSJV	Environmental Officer	Law Chun Ning, Goosiear	9625 2381	2682 2783
KRSJV	Environmental Supervisor	TBA	6592 3084	2682 2783
AUES	Environmental Team Leader	TW Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079

Legend:


CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

KRS JV (Main Contractor) –Kwan On-Richwell-SCG Joint Venture

SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

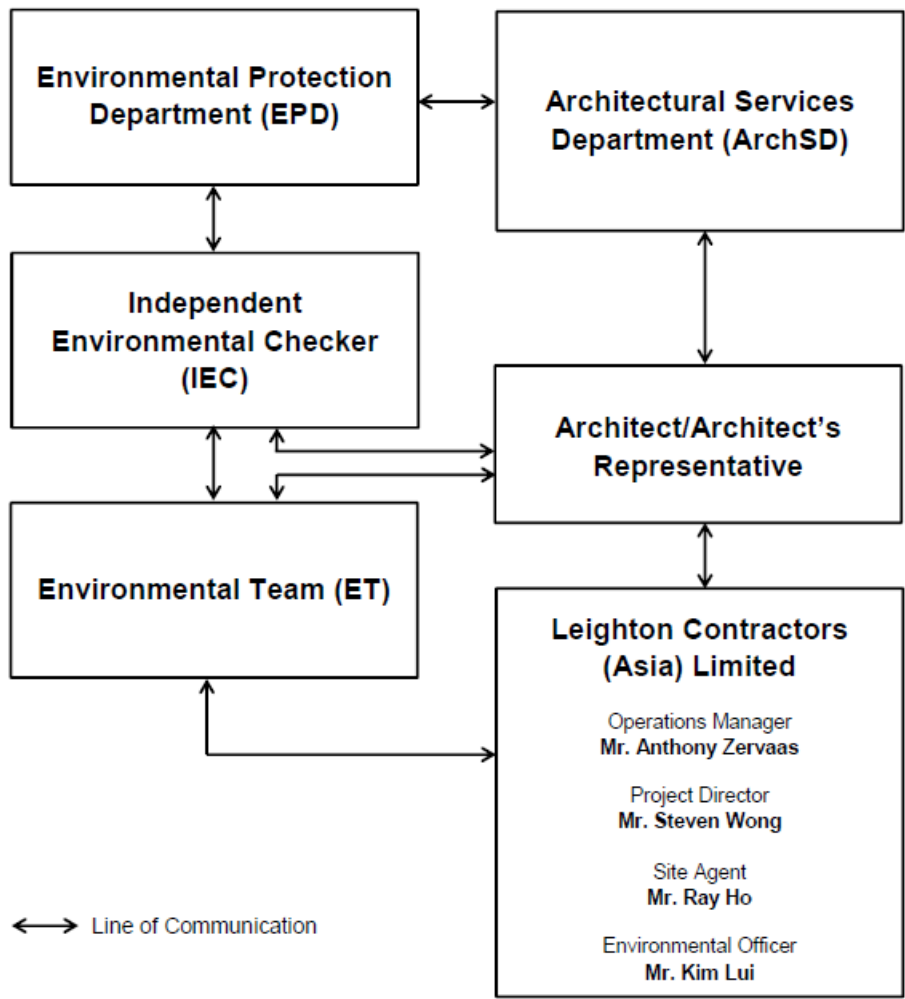

Environmental Management Organigram

Environmental Management Organization for Contract SS C505

Contact Details of Key Personnel for Contract SS C505

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
ArchSD	Works agent for the Development Bureau (DEVB)	Mr. William Cheng	2867 3904	2804 6805
Ronald Lu & Partners	Architect/ Architect's Representative	Mr. Justin Cheung	3189 9272	2834 5442
SMEC	Independent Environmental Checker	Mr. Antony Wong	3995 8120	3995 8101
Leighton	Operation Manager	Mr. Antony Zervaas	2823 1433	2529 8784
Leighton	Project Director	Mr. Steven Wong	2858 1519	2858 1899
Leighton	Site Agent	Mr. Ray Ho	2858 1519	2858 1899
Leighton	Environmental Officer	Mr. Legend Lam	3973 1003	-
Leighton	Assistant Environmental Officer	Mr. Alex Liu	3973 0818	-
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079

Legend:

ArchSD (Project Proponent) – Architectural Services Department

Ronald Lu & Partners (Architect/ Architect's Representative) – Ronald Lu & Partners (Hong Kong) Ltd

Leighton (Main Contractor) – Leighton Contractors (Asia) Limited

SMEC (IEC) – SMEC Asia Limited

AUES (ET) – Action-United Environmental Services & Consulting

Appendix C

3-month rolling construction program

Contract 2

Liantang / Heung Yuen Wai Boundary Control Point and Associated Works

CEDD Contract No: CV/2012/08

Main Contractor: Dragages Hong Kong Ltd



Tentative Three Months (Sep, Oct, Nov 2018) Construction Rolling Program

Item	Construction Activities
1	Admin Bldg - Building fit out, permanent drainage and E&M installation
2	Admin Bldg - Landscaping works
3	Mid-Vent Portal - Building fit out and E&M installation
4	Mid-Vent Portal - Construction of flexible barrier and permanent drainage
5	Mid-Vent Portal - Landscaping works.
6	North Portal - Construction of retaining wall, permanent drainage and slip road
7	North Portal - Tunnel backfilling, VE panel and E&M installation
8	North Portal - Construction of tunnel internal structure
9	North Portal - Landscaping works
10	North Portal - North ventilation building fit out and E&M installation
11	South Portal - Construction of tunnel internal structure, tunnel backfilling and E&M installation
12	South Portal - South ventilation building fit out and E&M installation
13	South Portal - Construction of flexible barrier
14	South Portal - Landscaping works.
15	South Portal - Backfilling and construction of slip road

Contract 3

Liantang / Heung Yuen Wai Boundary Control Point and Associated Works

CEDD Contract No: CV/2012/09

Main Contractor: Chun Wo Construction Ltd



俊和建築工程有限公司

CHUN WO CONSTRUCTION & ENGINEERING CO., LTD.

Tentative Three Months (September, October and November 2018) Construction Rolling Program

Item	Construction Activities
1	Cable detection and trial trenches
2	Remaining works on new Footbridge
3	Noise barrier construction
4	Road pavement works
5	Water main laying works (on Grade and on bridge deck)
6	Installation of Noise barrier steel column & panel, and sign gantry (on Grade and on bridge deck)
7	Road Drainage Works
8	Waterproofing works on bridge deck
9	Bitumen paving on bridge deck
10	Installation of movement joint on the bridge
11	Construction of retaining wall
12	Landscaping works

Contract 4

Liantang / Heung Yuen Wai Boundary Control Point and Associated Works
CEDD Contract No: NE/2014/02
Main Contractor: Siemens Ltd.



Tentative Three Months (Sep Oct and Nov 2018) Construction Rolling Program

Item	Construction Activites
1	E&M installation at admin building
2	E&M installation at Ventilation Building
3	E&A installation at OHVD in tunnel
4	High mast erection
5	Cladding installation at Cheung Shan Tunnel
6	Sign fabricaiton and Installation

Contract 6

Contract 7


Contract SS C505

Tentative Three Months (September, October and November 2018) Construction Rolling Program

Item	Construction Activities
1	Passenger Terminal Building (PTB) G/F - Plant Room Structure Works, Backfilling & Drainage, Under Ground Utilities, Fence Wall and On Grade Slab
2	PTB - ABWF Works & MEP Installation - Front/Back of House Area, External Staircases, Hall Block External Façade, Southern Entrance Construction, Major Plant Rooms
3	PTB - External Works incl. Building 21-24, M/F External Wall (Ewall), Roof & Upper Roof Roofing Works, Podium Coach Canopy, 21&22 (C&PC KIOSKS) & 23&24 (PC Examination Building & MSRVSS) Superstructure & ABWF Works and MEP Installation, Podium Open Area Waterproofing, Paving, Hard and Soft Landscaping works, Ambulance Canopy / Glazed Canopy
4	Bridge C Integrated ABWF and MEP Installation Works (C7 Portion)
5	Bldg 1 - C&ED Detector Dog Base Phase 1 - Integrated ABWF & MEP Works at G/F & R/F
6	Bldg 2 - HKPF Building and Observation Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to 4/F and Observation Tower (including Lift)
7	Bldg 3 - Fire Station and Drill Tower Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to UR/F, Drill Tower
8	Bldg 4 - Cargo Examination Building (Inbound) Phase 1 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
9	Bldg 5 - Cargo Examination Building (Outbound) Phase 2 - External Works, Integrated ABWF & MEP Works at G/F to R/F, Loading Dock
10	Bldg 6 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Inbound) - External Works Fence Wall, Integrated ABWF & MEP Works at G/F to R/F
11	Bldg 7 - Fixed X-ray Vehicle Inspection System (FXRVIS) Buildings (Outbound) - Integrated ABWF & MEP Works at G/F
12	Bldg 8 - MXRVSS (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & R/F
13	Bldg 9 - MXRVSS (Outbound) Phase 2 - Structure Works at G/F, Integrated ABWF and MEP Works at G/F & Envelope
14	Bldg 10 - GV Kiosk (Inbound) Phase 2 - On-Grade Slab, Steel Structure Works, Integrated ABWF and MEP Works at G/F & R/F
15	Bldg 11 - GV Kiosk (Outbound) Phase 2 - Steel Structure Works, Integrated ABWF & MEP Works at G/F & R/F
16	Bldg 12 - Public Toilets (Inbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
17	Bldg 13 - Public Toilets (Outbound) Phase 2 - Structures Works, Integrated ABWF and MEP Works at G/F & R/F
18	Bldg 14 - Disinsection Facilities (Inbound) Phase 2 - Integrated ABWF & MEP Works at G/F & Envelope
19	Bldg 15 - Disinsection Facilities (Outbound) Phase 2 - Substructure and Structure Works, Integrated ABWF & MEP Works at G/F & Envelope
20	Bldg 16 - Weigh Station Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
21	Bldg 17 - EUVSS & Monitoring Room Phase 2 - Structure Works, Integrated ABWF & MEP Works at G/F & R/F
22	Bldg 18 - Refuse Collection Point Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
23	Bldg 25 - Traffic Control Office (Inbound) Phase 2 - Integrated ABWF and MEP Works at G/F & Envelope
24	Bldg 26 - Traffic Control Office (Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
25	Bldg 27 - Inspection Post Phase 2 - Structure Works, Integrated ABWF and MEP Work at G/F & Envelope
26	Bldg 28, 30 & 31 - Guard Booth (Inbound/Outbound) Phase 2 - Structure Works, Integrated ABWF and MEP Works at G/F & Envelope
27	Bldg 32 to 35 - Steel Canopies Phase 2 - Structure Works, Integrated ABWF and MEP Works
28	Bldg 37 to 40 - Elevated Walkway (E1, E2, E3 & E4) Phase 2 - Structures Works, ABWF and BS Works
29	Vehicular bridges 1 to 5 Phase 3 - Retaining walls, Road and Finishes Works
30	External Works - CLP Cable & Power ON Transfer room
31	External Works - Water Meter Room Connection (Inbound & Outbound)
32	External Works - External Utilities, UU works & DSD Inspection
33	External Works - Road & Pavement Works
34	Landscape - Inbound Area
35	Testing & Commissioning (T&C) and FSD Inspection - CBO, FXO, Inbound & Outbound Group Buildings

Appendix D

Designated Monitoring Locations as Recommended in the Approved EM&A Manual

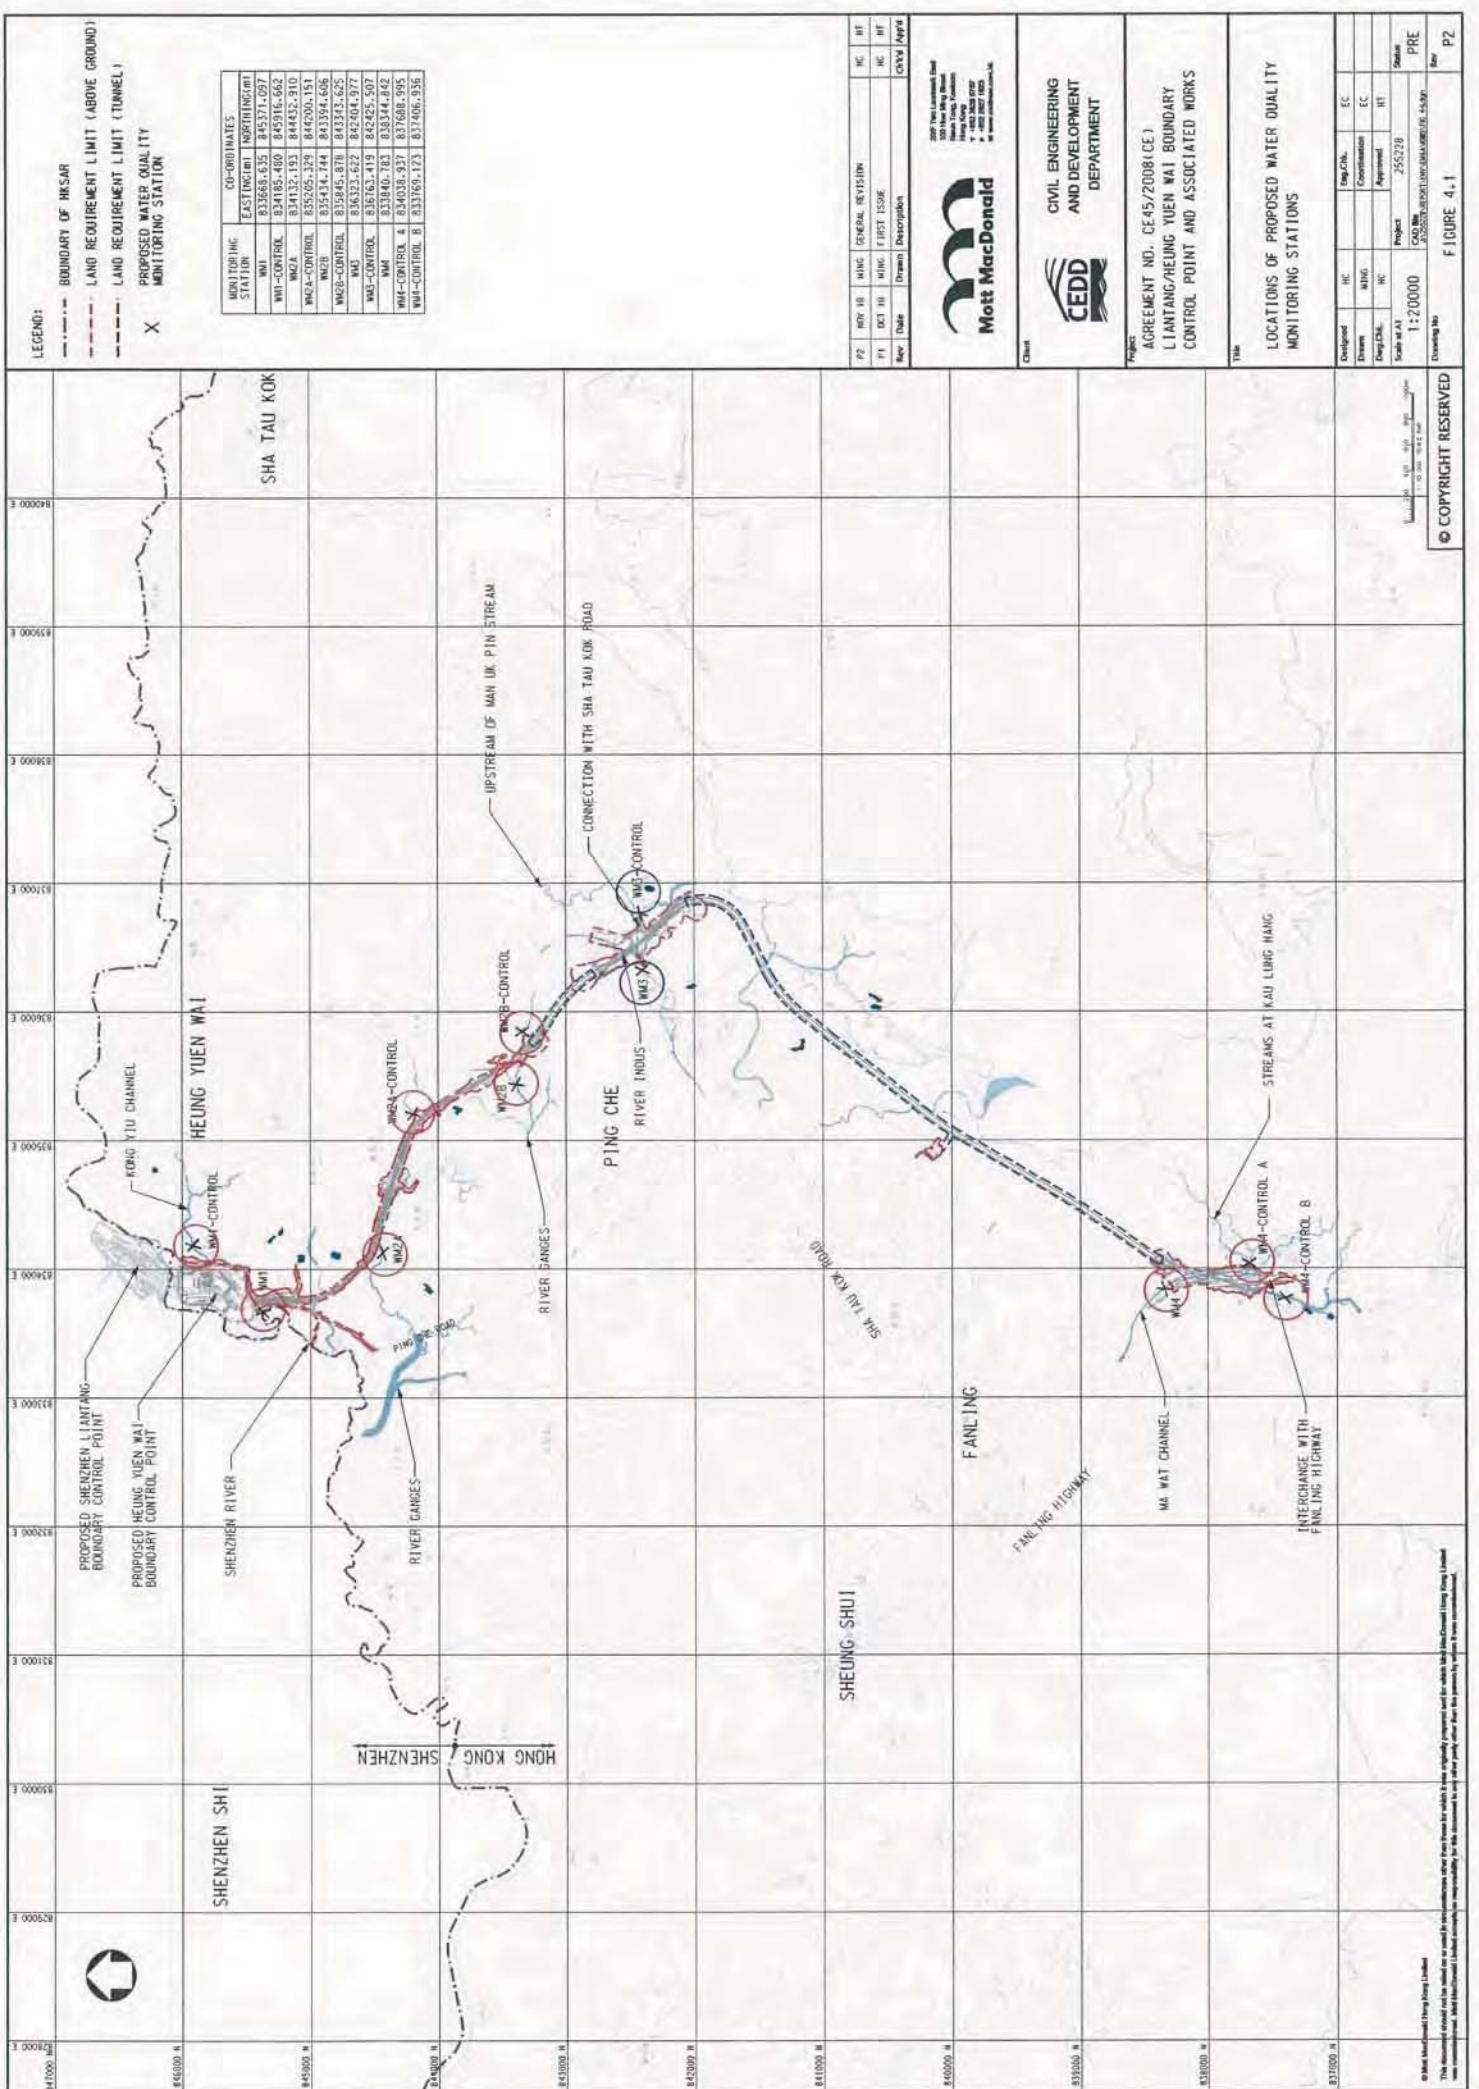

LEGEND:

- BOUNDARY OF HK SAR
- LAND REQUIREMENT LIMIT (ABOVE GROUND)
- LAND REQUIREMENT LIMIT (TUNNEL)
- X PROPOSED WATER QUALITY MONITORING STATION

MONITORING STATION	CO-ORDINATES	
	EASTING	NORTHING
WMA	837668.635	845371.097
WMA-CONTROL	834185.460	845916.662
WMA	834132.193	844432.910
WMA-CONTROL	835205.329	844200.151
WMA	835134.744	843384.606
WMA-CONTROL	835945.878	843343.625
WMA	836332.622	842404.977
WMA-CONTROL	836163.419	842425.507
WMA	833840.763	838344.842
WMA-CONTROL 4	834038.937	837688.995
WMA-CONTROL 8	833769.123	837406.936

P2	REV 18	MISC	GENERAL REVISION	HC	HT
P1	DEC 10	MISC	FIRST ISSUE	HC	HT
Rev	Date	Drawn	Description	HC	HT



CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

PROJECT AGREEMENT NO. CE 45/2008(CE)
LIANTANG/YUEN WAI BOUNDARY CONTROL POINT AND ASSOCIATED WORKS

TITLE LOCATIONS OF PROPOSED WATER QUALITY MONITORING STATIONS


Drawn	HC	HT	EC
Checked	WJG		EC
Design	HC		HT
Scale	1:20000	Project	255278
Drawn No	255203	CAU No	004/06/03/15/09
Drawn Date		State	PRE
Drawn By		Rev	P2

© COPYRIGHT RESERVED

This document is confidential and its use is restricted to the project for which it was prepared. It is not to be distributed, copied, or used for any other purpose without the prior written consent of Mott MacDonald.

Appendix E

Monitoring Locations for Impact Monitoring

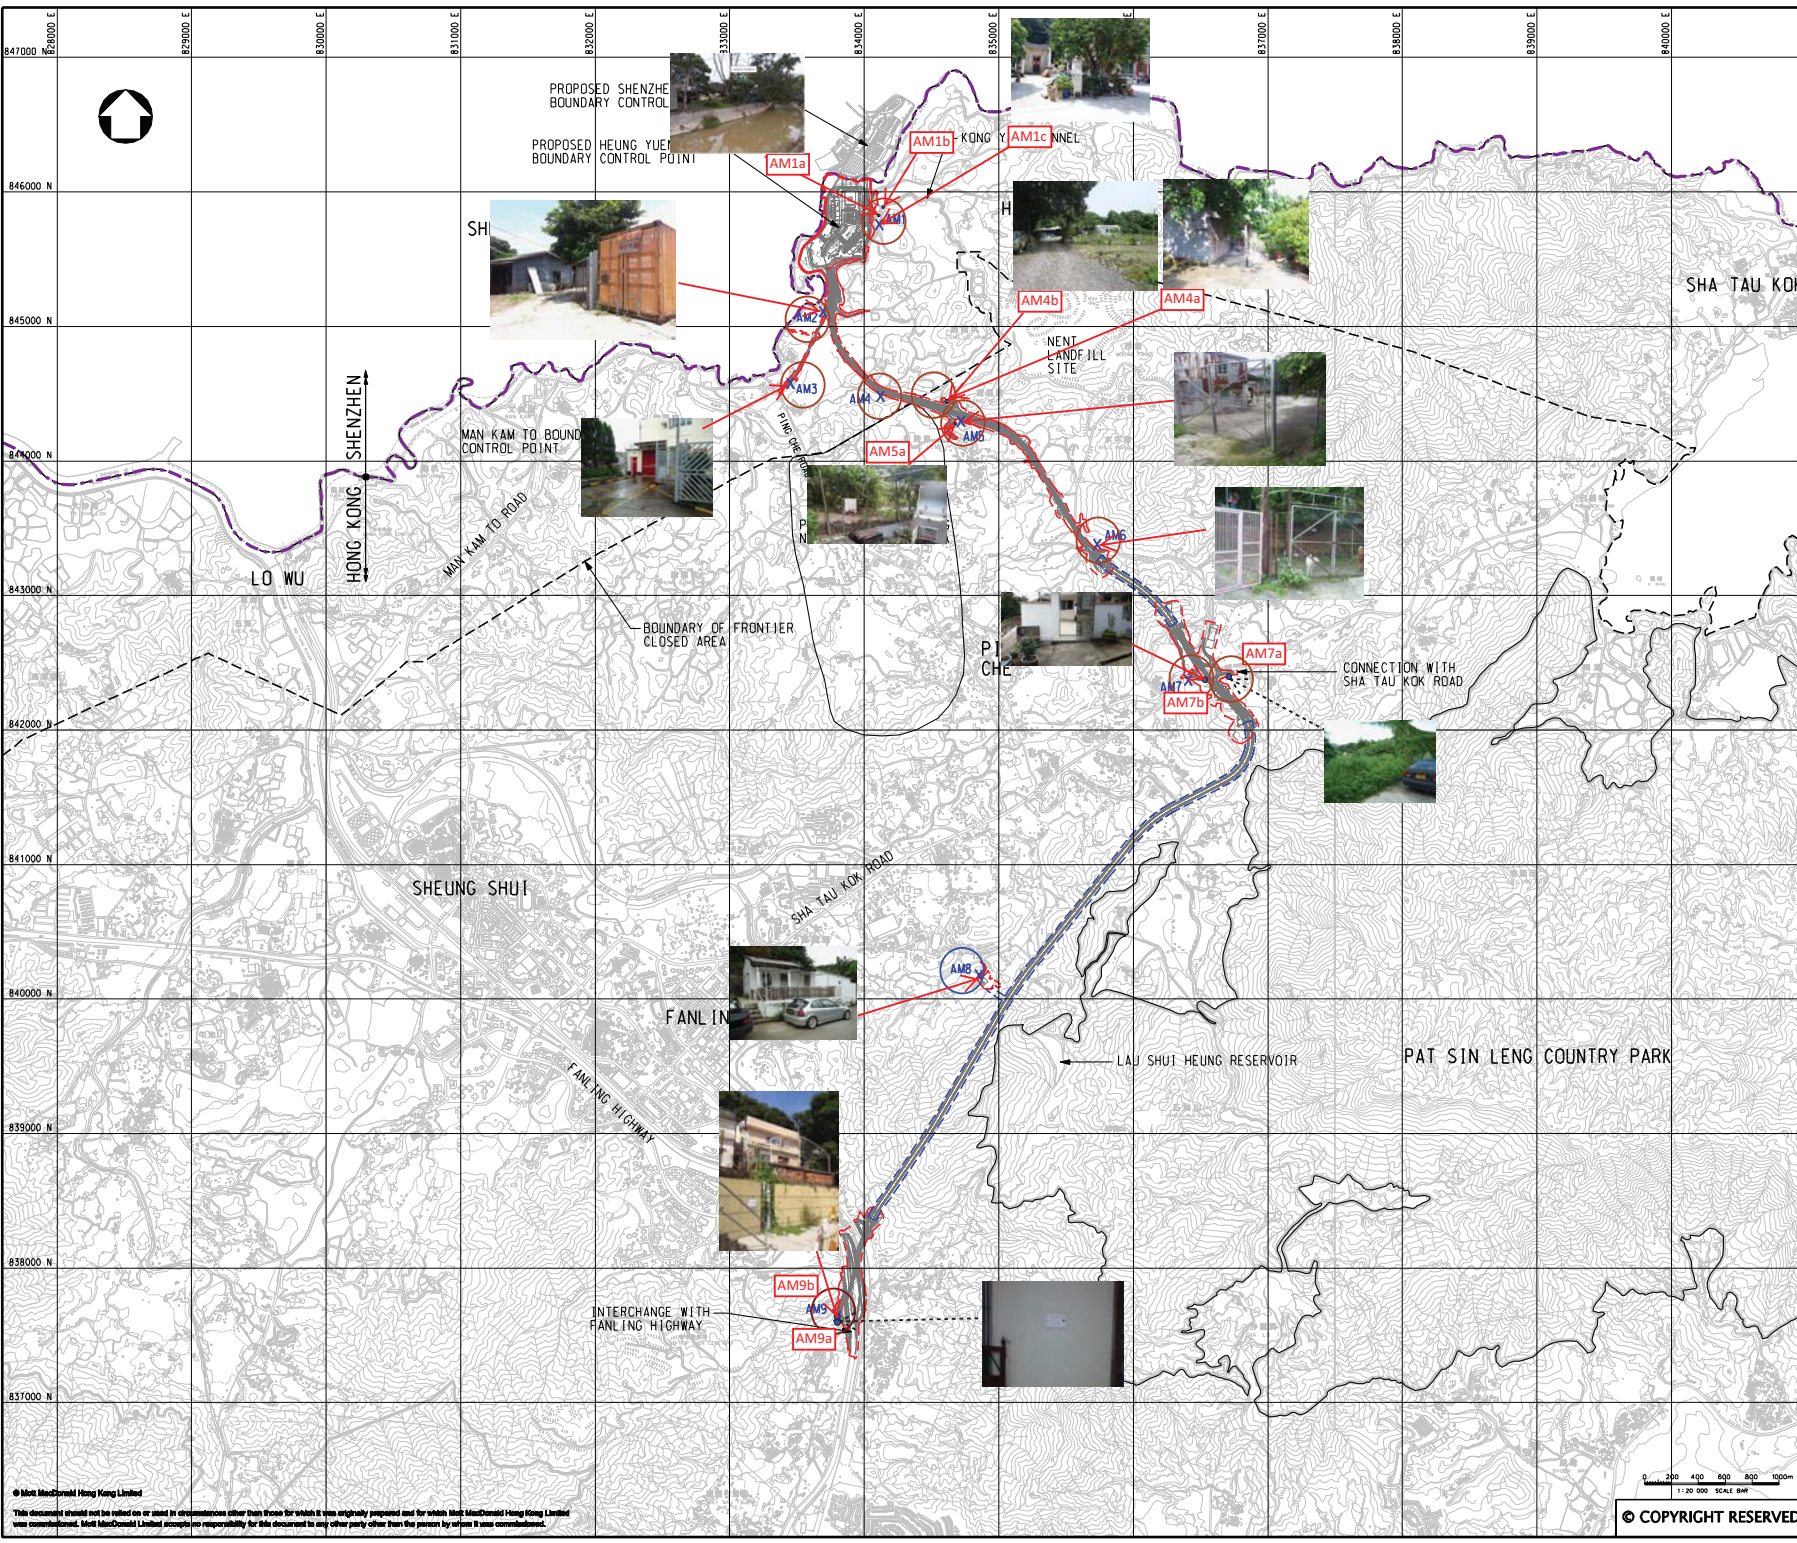


- LEGEND:**
- BOUNDARY OF HKSAR
 - WORKS AREA (ABOVE GROUND)
 - WORKS AREA (TUNNEL)
 - X Air Monitoring Stations in the EM&A Manual
 - Proposed Air Monitoring Stations

P1	AUG 10	MING	FIRST ISSUE	DC	HT
Rev	Date	Drawn	Description	Chk'd	App'd



20/F Two Landmark East
100 Houshang Street
Kowloon, Hong Kong
T +852 2518 5757
F +852 2827 1823
W www.mottmac.com.hk

Client



CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

Project
 AGREEMENT NO. CE45/2008(CE)
 LIANTANG/HEUNG YUEN WAI BOUNDARY CONTROL POINT AND ASSOCIATED WORKS

Title
 PROPOSED LOCATION OF CONSTRUCTION AIR QUALITY MONITORING STATIONS


Designed	DC	Eng.Chk.	EC	
Drawn	MING	Coordination	EC	
Draw.Chk.	DC	Approved	HT	
Scale at A1	1:20000	Project	255228	Status
		CAD file	255228\report\env\em&a\00831\FE_21.dgn	PRE
Drawing No				Rev
				P1

© Mott MacDonald Hong Kong Limited

This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.

© COPYRIGHT RESERVED

FIGURE 2.1

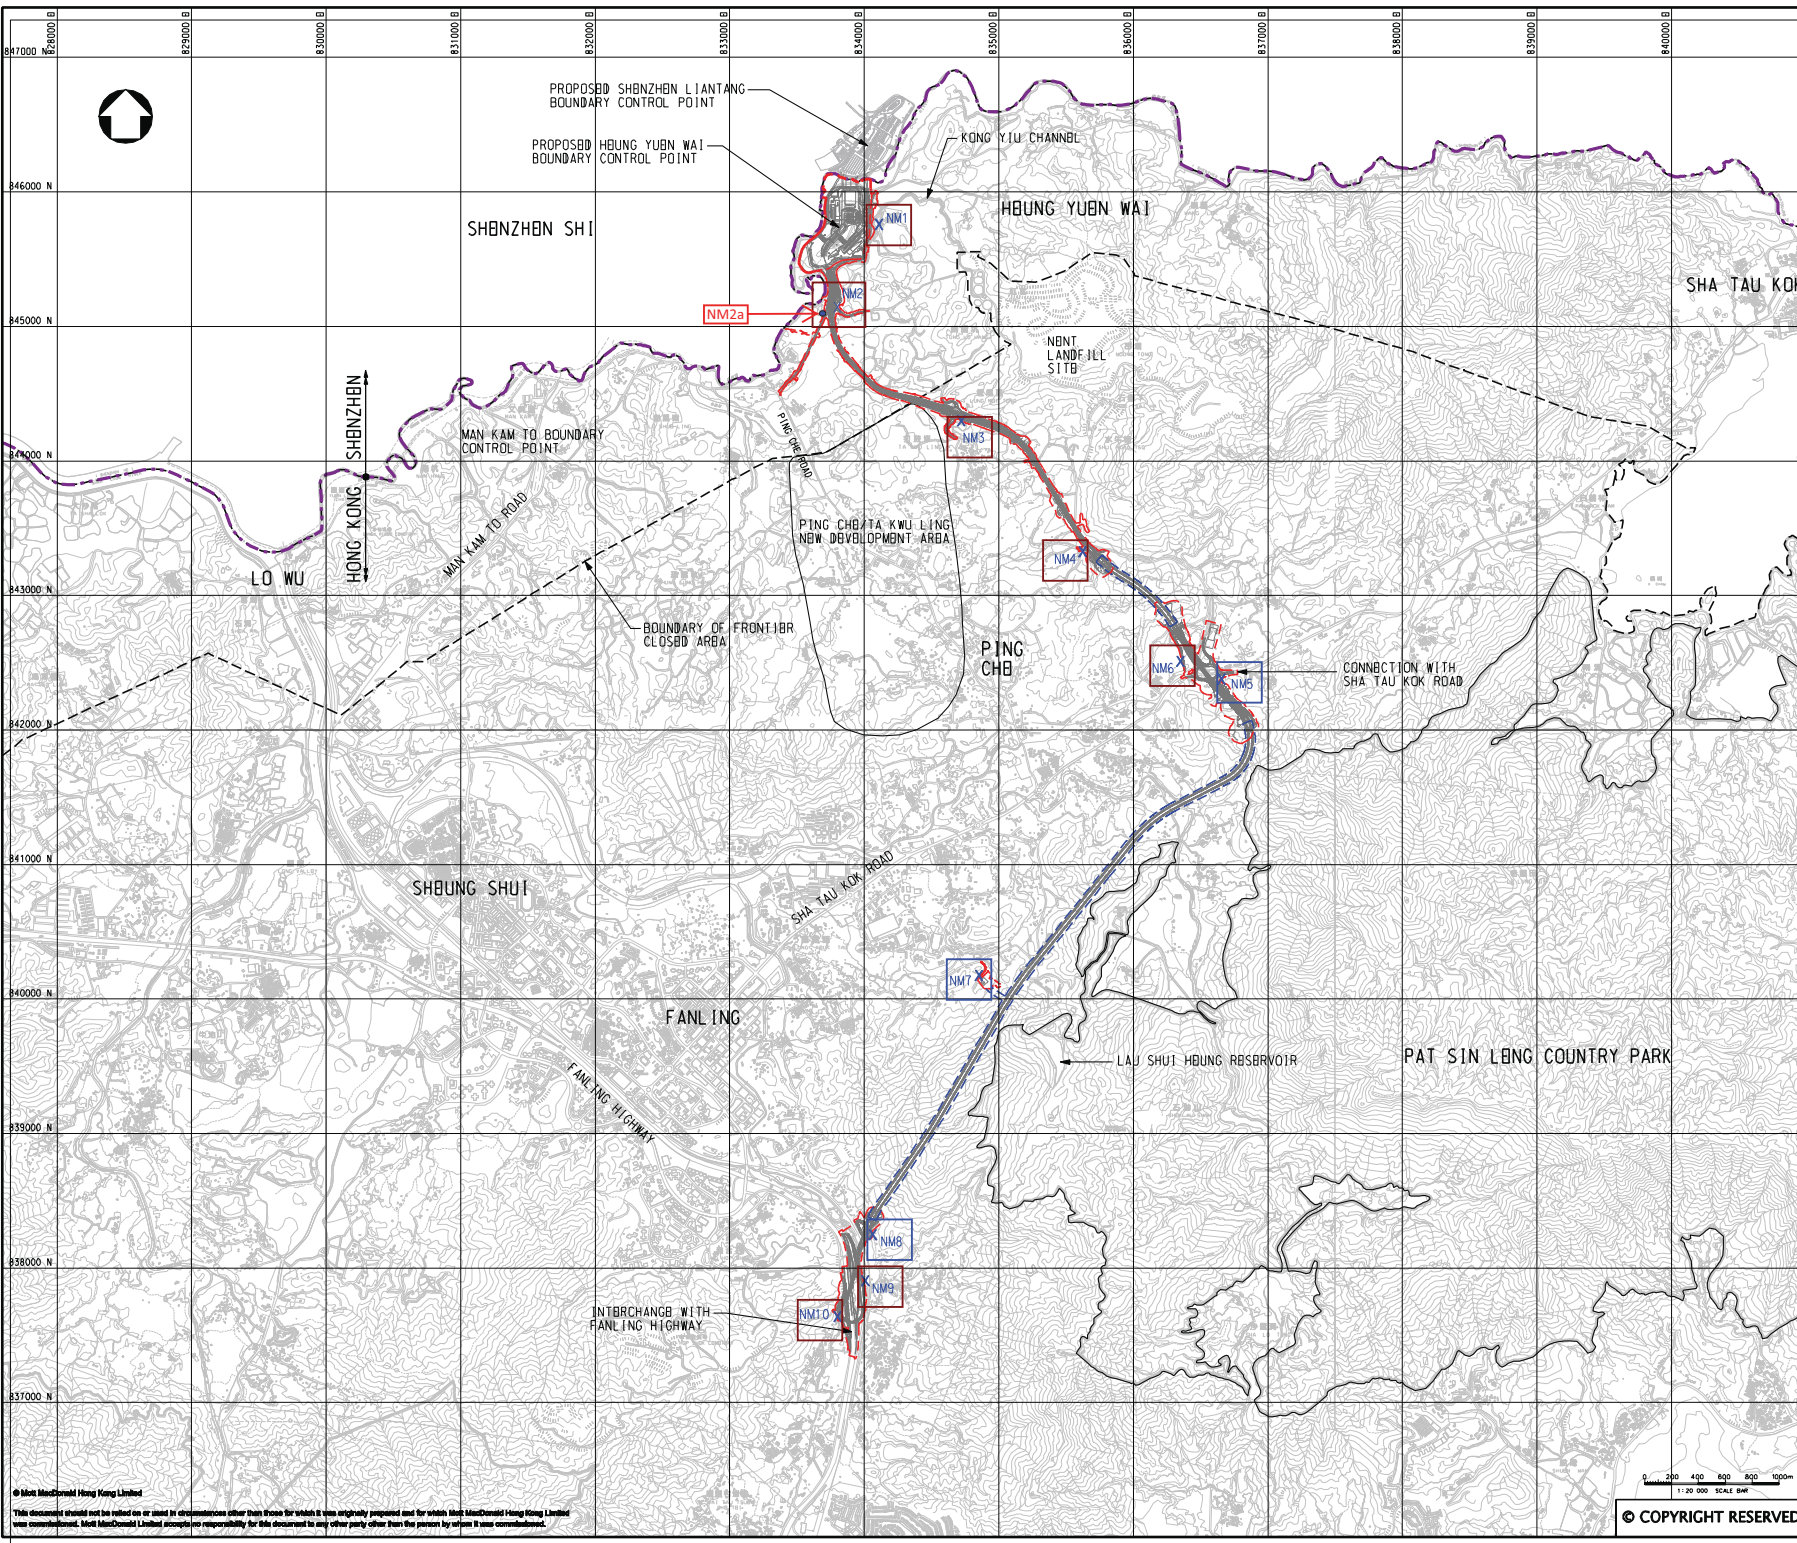


- LEGEND:**
- BOUNDARY OF HKSAR
 - WORKS AREA (ABOVE GROUND)
 - WORKS AREA (TUNNELL)
 - X CONSTRUCTION NOISE MONITORING STATIONS
 - Proposed Noise Monitoring Stations

P1	AUG 10	MING	FIRST ISSUE	DC	HT
Rev	Date	Drawn	Description	CHK'd	App'd



20/F Two Landmark East
100 Housiang Street
Kowloon, Kowloon
Hong Kong
T +852 2518 5757
F +852 2827 1823
W www.mottmac.com.hk

Client




CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

Project
 AGREEMENT NO. CB45/2008(CB)
 LIANTANG/HUNG YUEN WAI BOUNDARY CONTROL POINT AND ASSOCIATED WORKS

Title
 PROPOSED LOCATION OF CONSTRUCTION NOISE MONITORING STATIONS

Designed	DC	Eng.Chk.	BC	
Drawn	MING	Coordination	BC	
Dep.Chk.	DC	Approved	HT	
Scale of A1	1:20000	Project	255228	Status
		CAD file	255228\report\env\env\ca\00831\FE_31.dgn	PRB
Drawing No				Rev
				P1

© Mott MacDonald Hong Kong Limited
 This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.

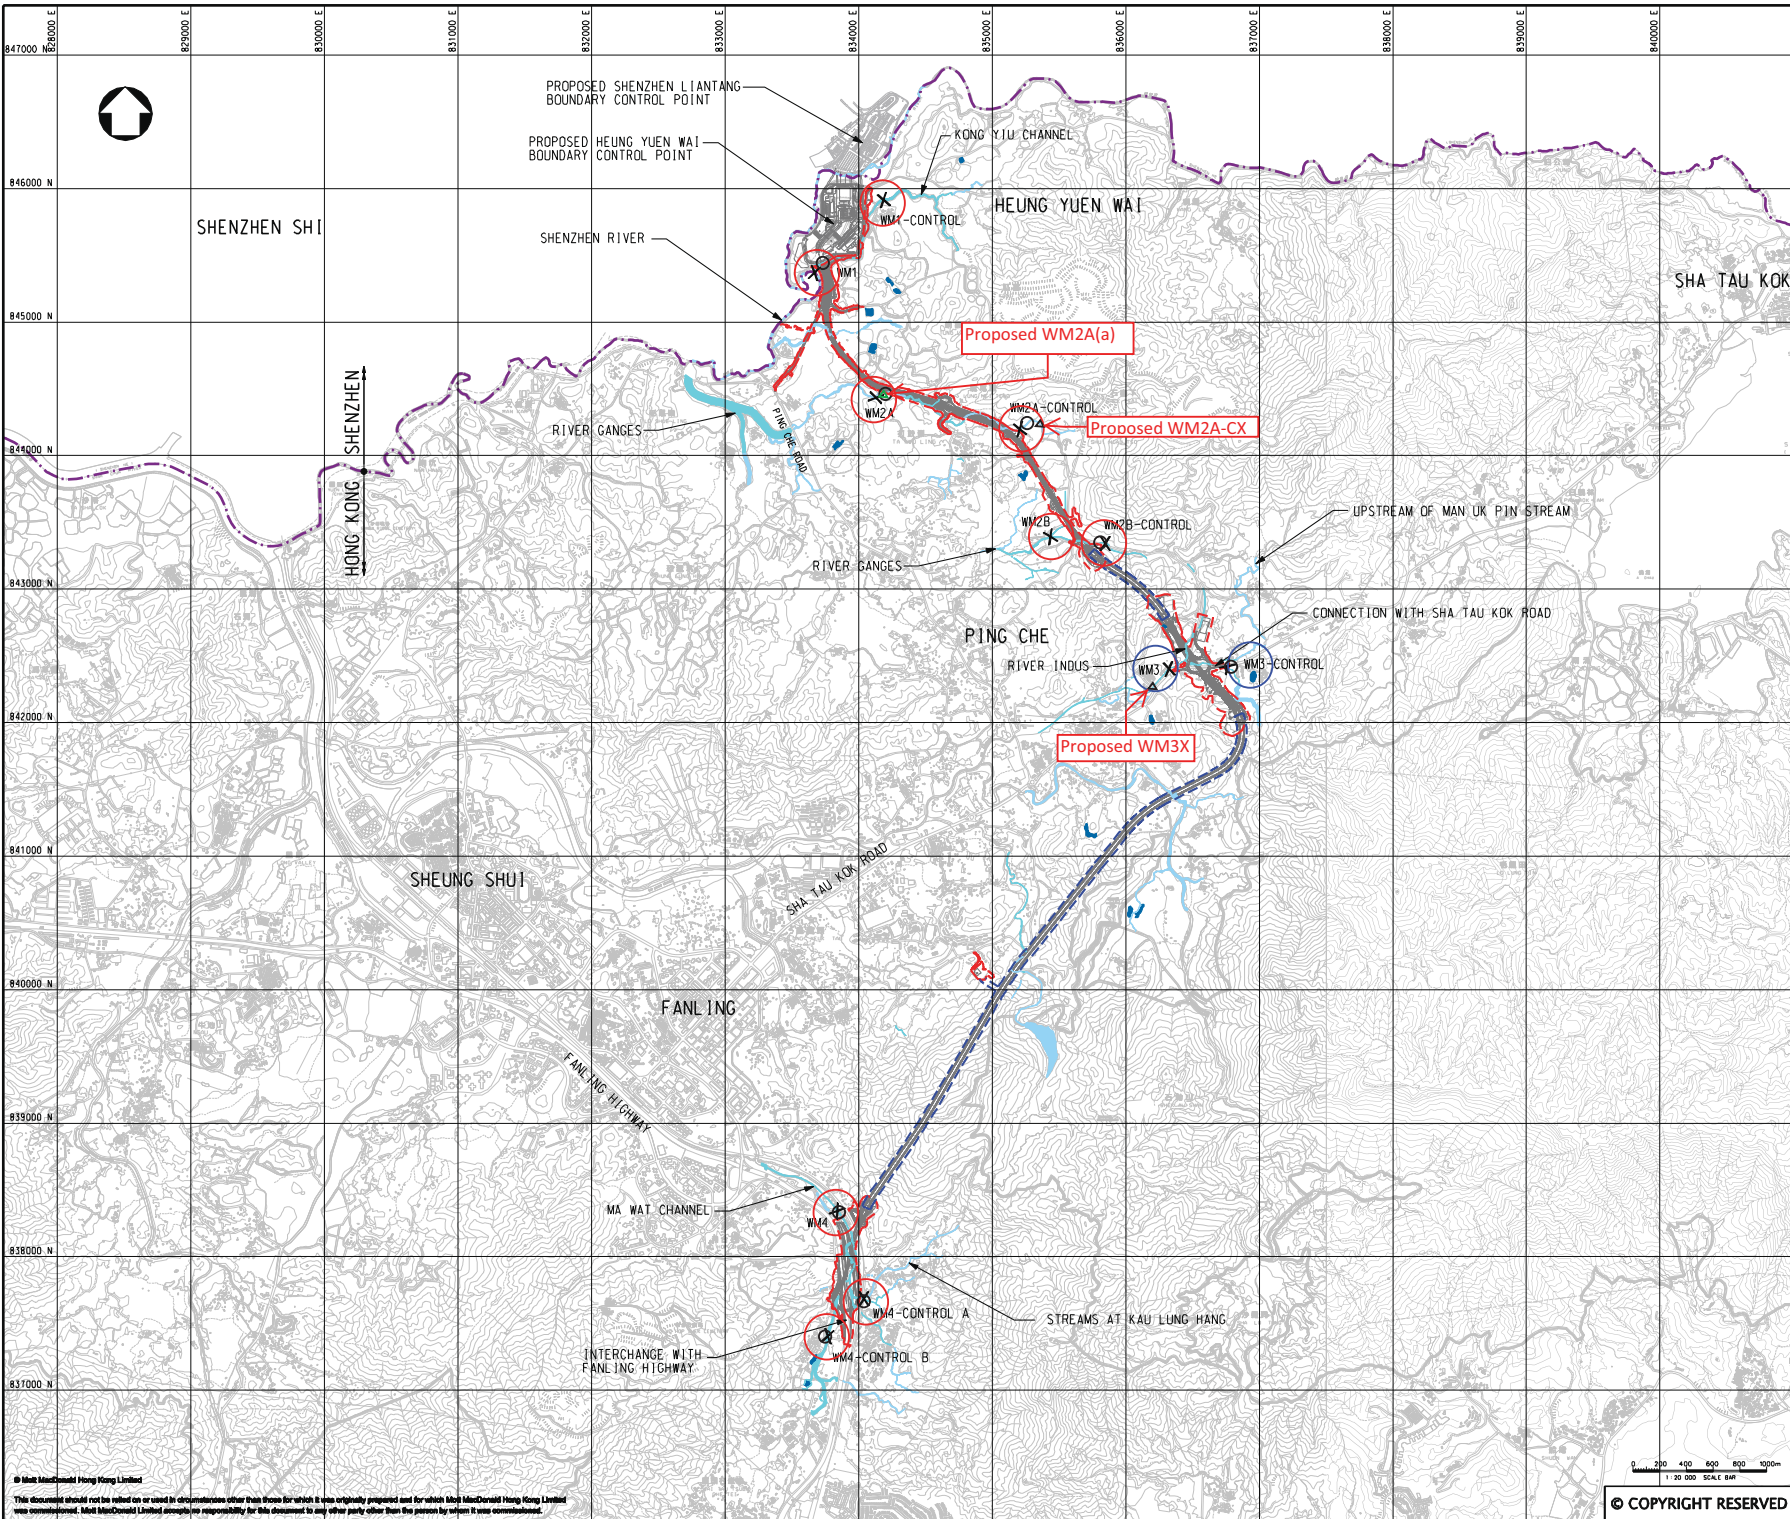

- LEGEND:**
- BOUNDARY OF HKSAR
 - LAND REQUIREMENT LIMIT (ABOVE GROUND)
 - LAND REQUIREMENT LIMIT (TUNNEL)
 - X Water Quality Monitoring Location Recommended in EM&A Manual
 - Alternative Water Quality Monitoring Location for EM&A Programme
 - △ New Proposed Water Quality Monitoring Location in November 2015
 - ▲ New Proposed Water Quality Monitoring Location in May 2016

Station ID	Location recommended in EM&A Manual		Location found during site visit	
	Coordinates		Coordinates	
	Easting	Northing	Easting	Northing
WM1	83456.835	84577.072	83457.1	84542.1
WM1-Control	83418.480	84591.662	83418.5	84517.3
WM2A	83418.319	84412.910	83420.4	84417.3
WM2A-Control	83505.329	84420.151	83527.0	84424.5
WM2B	83543.744	84339.606	83543.5	84339.7
WM2B-Control	83545.878	84343.625	83535.1	84355.1
WM3	83623.622	84404.377	83624.0	84402.7
WM3-Control	83673.415	84242.507	83673.5	84240.0
WM4	83840.781	83834.842	83850.0	83838.0
WM4-Control A	83408.837	83764.895	83402.8	83765.0
WM4-Control B	83769.123	83740.936	83760.0	83739.5

New Proposed Water Quality Monitoring Location in November 2015

Location ID	Easting	Northing
WM2A-C (Original)	0835270	0844243
WM2A-Cx (Proposed)	0835377	0844188
WM3 (Original)	0836324	0842402
WM3x (Proposed)	0836206	0842270

New Proposed Water Quality Monitoring Location in May 2016

Location ID	Easting	Northing
WM2A (Original)	834204	844471
WM2A(a) (Proposed)	834191	844474

Rev	Date	Drawn	Description	CHK'd	App'd
P2	NOV 10	MING	GENERAL REVISION	HC	HT
P1	OCT 10	MING	FIRST ISSUE	HC	HT

2007 Two Landmark East
100 New King Street
Kowloon, Hong Kong
Tel: +852 2502 8787
Fax: +852 2827 1823
www.mottmac.com.hk

Client

CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

Project
 AGREEMENT NO. CE45/2008 (CE)
 LIANTANG/HEUNG YUEN WAI BOUNDARY CONTROL POINT AND ASSOCIATED WORKS

Title
 LOCATIONS OF PROPOSED WATER QUALITY MONITORING STATIONS

Designed	HC	Eng.Chk.	EC
Drawn	MING	Coordination	EC
Dwg.Chk.	HC	Approved	HT
Scale at A1	Project 255228		Status
1:20000	CAD file: S:\255228\REPORTS\EM&A\WQMS\LOC_A1.dgn		PRE
Drawing No	Appendix C		Rev
			P2

© Mott MacDonald Hong Kong Limited
 This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Limited accepts no responsibility for this document to any other party other than the person to whom it was commissioned.

Appendix F

Calibration Certificate of Monitoring Equipment and HOKLAS-accreditation Certificate of the Testing Laboratory

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Open area at Tsung Yuen Ha Village	Date of Calibration: 26/7/2018
Location ID : AM1c	Next Calibration Date: 26/9/2018
	Technician: Eric

CONDITIONS

Sea Level Pressure (hPa) 1006.5	Corrected Pressure (mm Hg) 754.875
Temperature (°C) 29.6	Temperature (K) 303

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope -> 2.02017
Model-> 5025A	Qstd Intercept -> -0.03691
Serial # -> 1612	

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION		
							Slope =	Intercept =	Corr. coeff. =
18	5.6	5.6	11.2	1.657	46	45.49	27.9821	-0.3045	0.9976
13	4.4	4.4	8.8	1.471	42	41.54			
10	3.4	3.4	6.8	1.295	36	35.60			
7	2.2	2.2	4.4	1.045	30	29.67			
5	1.3	1.3	2.6	0.808	22	21.76			

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

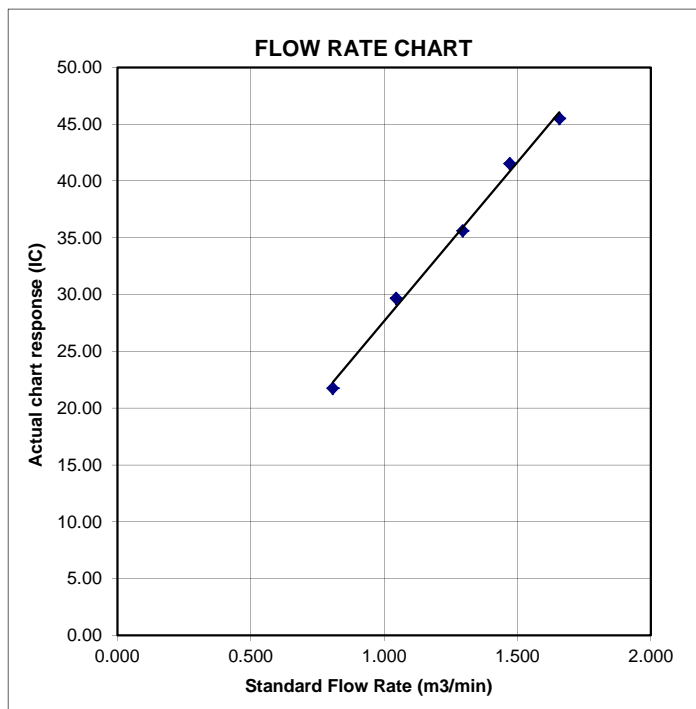

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Open area at Tsung Yuen Ha Village	Date of Calibration:	24/9/2018
Location ID : AM1c	Next Calibration Date:	24/11/2018
	Technician:	Eric

CONDITIONS

Sea Level Pressure (hPa)	1011.1	Corrected Pressure (mm Hg)	758.325
Temperature (°C)	27.0	Temperature (K)	300

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope ->	2.02017
Model-> 5025A	Qstd Intercept ->	-0.03691
Serial # -> 1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION		
							Slope =	Intercept =	Corr. coeff. =
18	5.5	5.7	11.2	1.668	46	45.80	Slope =	27.5780	
13	4.4	4.4	8.8	1.480	42	41.81	Intercept =	0.2924	
10	3.5	3.3	6.8	1.303	36	35.84	Corr. coeff. =	0.9981	
7	2.2	2.2	4.4	1.052	30	29.87			
5	1.2	1.3	2.5	0.797	22	21.90			

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

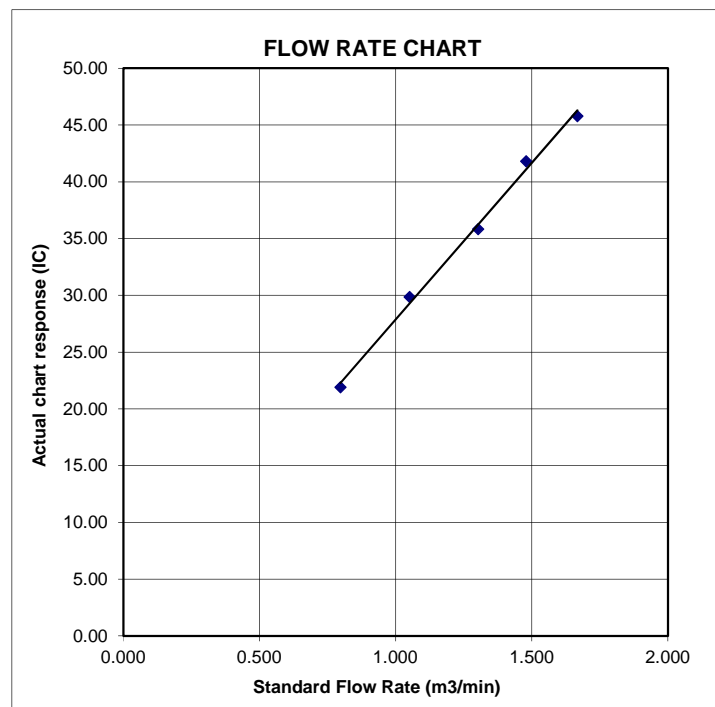

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Village House near Lin Ma Hang Road
 Location ID : AM2

Date of Calibration: 8/8/2018
 Next Calibration Date: 8/10/2018
 Technician: Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	4.9	4.9	9.8	1.547	50	49.34	Slope = 31.7234 Intercept = -0.8916 Corr. coeff. = 0.9940
13	4.1	4.1	8.2	1.417	44	43.42	
10	3.2	3.2	6.4	1.254	38	37.50	
7	2	2	4.0	0.995	32	31.58	
5	1.3	1.3	2.6	0.806	25	24.67	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

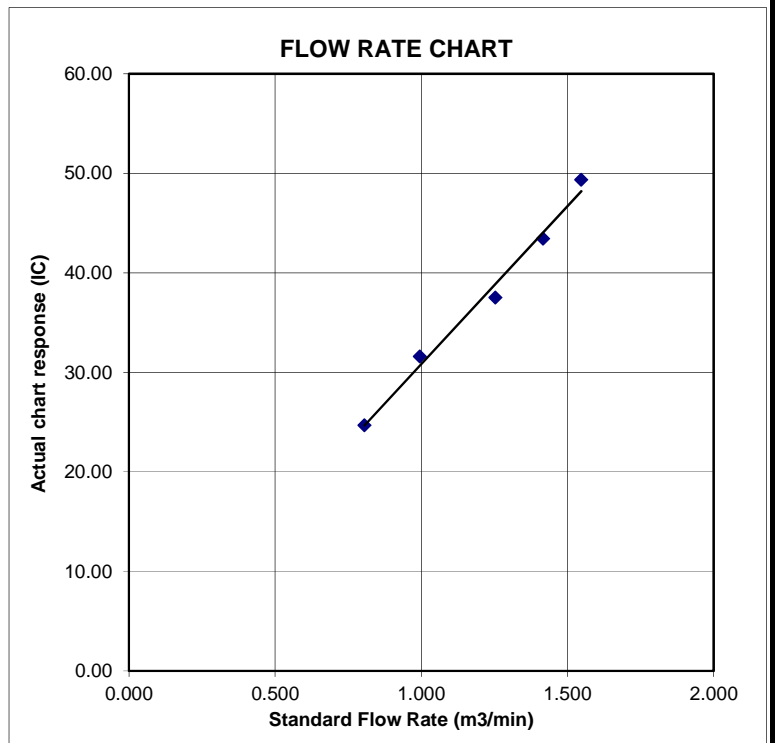

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Ta Kwu Ling Fire Service Station	Date of Calibration:	8/8/2018
Location ID : AM3	Next Calibration Date:	8/10/2018
	Technician:	Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.6	5.6	11.2	1.653	50	49.34	Slope = 26.7072 Intercept = 5.3642 Corr. coeff. = 0.9963
13	4.4	4.4	8.8	1.467	46	45.39	
10	3.4	3.4	6.8	1.292	40	39.47	
7	2.1	2.1	4.2	1.019	32	31.58	
5	1.3	1.3	2.6	0.806	28	27.63	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

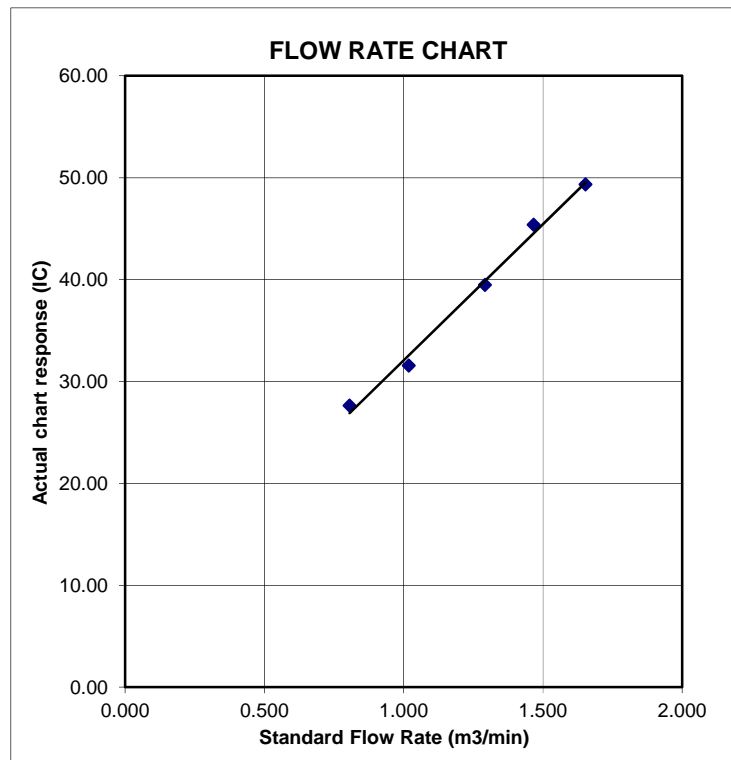

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Nga Yiu Ha Village	Date of Calibration:	8/8/2018
Location ID : AM4b	Next Calibration Date:	8/10/2018
	Technician:	Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.5	5.5	11.0	1.638	54	53.28	Slope = 31.2497 Intercept = 1.8456 Corr. coeff. = 0.9992
13	4.4	4.4	8.8	1.467	48	47.36	
10	3.3	3.3	6.6	1.273	42	41.44	
7	2	2	4.0	0.995	34	33.55	
5	1.4	1.4	2.8	0.836	28	27.63	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

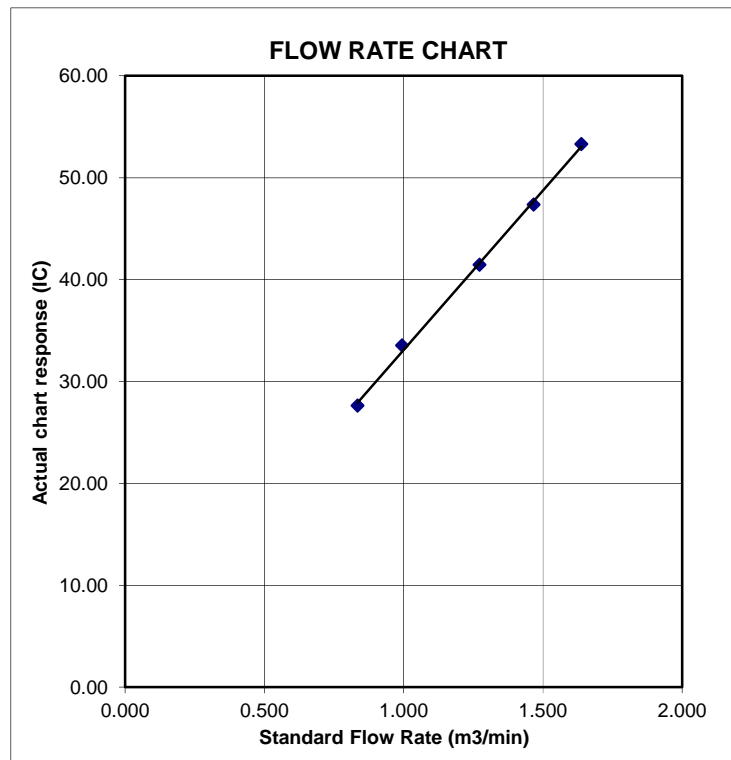

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Ping Yeung Village House	Date of Calibration:	8/8/2018
Location ID : AM5a	Next Calibration Date:	8/10/2018
	Technician:	Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.8	5.8	11.6	1.682	44	43.42	Slope = 36.9710 Intercept = -19.0002 Corr. coeff. = 0.9965
13	4.5	4.5	9.0	1.484	35	34.54	
10	3.4	3.4	6.8	1.292	30	29.60	
7	2.2	2.2	4.4	1.043	21	20.72	
5	1.3	1.3	2.6	0.806	10	9.87	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

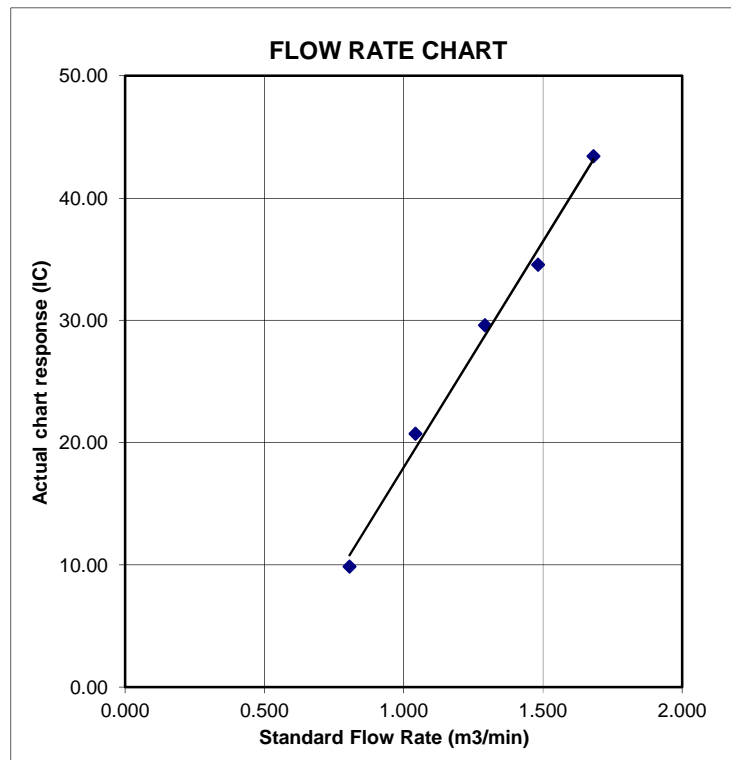

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Wo Keng Shan Village House	Date of Calibration:	8/8/2018
Location ID : AM6	Next Calibration Date:	8/10/2018
	Technician:	Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.3	5.3	10.6	1.609	52	51.31	Slope = 30.7268 Intercept = 0.3083 Corr. coeff. = 0.9940
13	4.6	4.6	9.2	1.500	46	45.39	
10	3.5	3.5	7.0	1.311	40	39.47	
7	2.1	2.1	4.2	1.019	32	31.58	
5	1.3	1.3	2.6	0.806	26	25.66	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

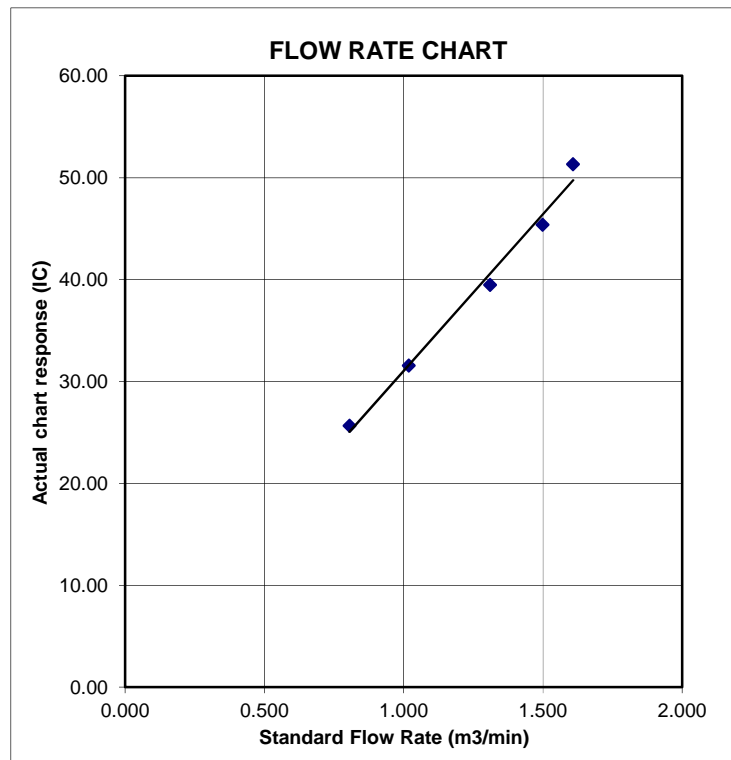

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Village House of Loi Tung Village

Date of Calibration: 8/8/2018

Location ID : AM7b

Next Calibration Date: 8/10/2018

Technician: Fai So

CONDITIONS

Sea Level Pressure (hPa) 1004.2
 Temperature (°C) 30.3

Corrected Pressure (mm Hg) 753.15
 Temperature (K) 303

CALIBRATION ORIFICE

Make-> TISCH
 Model-> 5025A
 Serial # -> 1612

Qstd Slope -> 2.02017
 Qstd Intercept -> -0.03691

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.4	5.4	10.8	1.623	54	53.28	Slope = 37.7511 Intercept = -8.6603 Corr. coeff. = 0.9982
13	4.6	4.6	9.2	1.500	48	47.36	
10	3.4	3.4	6.8	1.292	40	39.47	
7	2.2	2.2	4.4	1.043	32	31.58	
5	1.5	1.5	3.0	0.864	24	23.68	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

FLOW RATE CHART

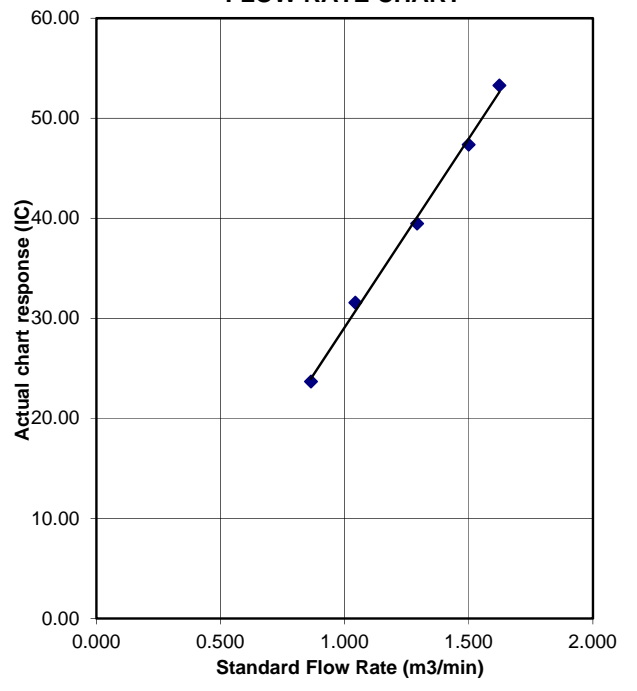

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Po Kat Tsai Village No. 4
 Location ID : AM8

Date of Calibration: 8/8/2018
 Next Calibration Date: 8/10/2018
 Technician: Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Serial # ->	1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION Slope = 43.9506 Intercept = -17.6019 Corr. coeff. = 0.9952
18	6.1	6.1	12.2	1.724	58	57.23	
13	4.8	4.8	9.6	1.532	50	49.34	
10	3.6	3.6	7.2	1.329	44	43.42	
7	2.4	2.4	4.8	1.088	30	29.60	
5	1.5	1.5	3.0	0.864	20	19.73	

Calculations :

$$Q_{std} = 1/m[\text{Sqrt}(H_2O(P_a/P_{std})(T_{std}/T_a))-b]$$


$$IC = I[\text{Sqrt}(P_a/P_{std})(T_{std}/T_a)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/T_{av})(P_{av}/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

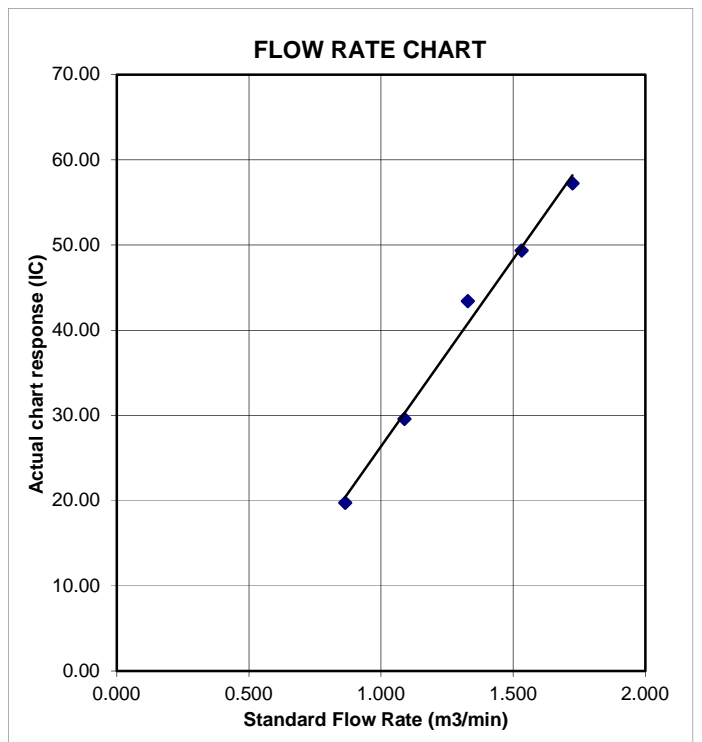

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Nam Wa Po Village House No. 80	Date of Calibration:	8/8/2018
Location ID : AM9b	Next Calibration Date:	8/10/2018
	Technician:	Fai So

CONDITIONS

Sea Level Pressure (hPa)	1004.2	Corrected Pressure (mm Hg)	753.15
Temperature (°C)	30.3	Temperature (K)	303

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope ->	2.02017
Model-> 5025A	Qstd Intercept ->	-0.03691
Serial # -> 1612		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.8	5.8	11.6	1.682	55	54.27	Slope = 36.6903 Intercept = -8.6996 Corr. coeff. = 0.9952
13	4.7	4.7	9.4	1.516	46	45.39	
10	3.6	3.6	7.2	1.329	40	39.47	
7	2.3	2.3	4.6	1.066	32	31.58	
5	1.5	1.5	3.0	0.864	23	22.70	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

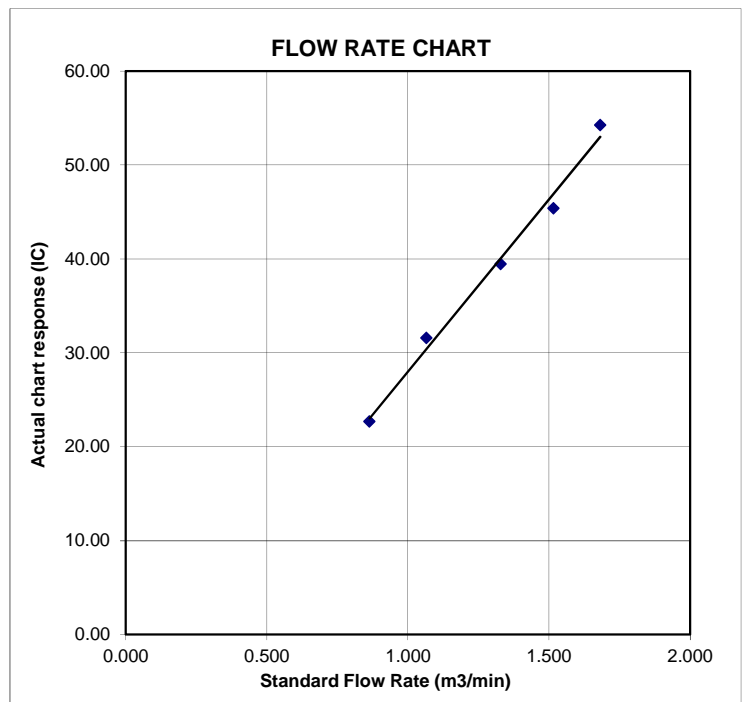

Certificate of Calibration

Calibration Certification Information			
Cal. Date: February 13, 2018	Rootsmeter S/N: 438320	Ta: 293	°K
Operator: Jim Tisch		Pa: 763.3	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: 1612		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3970	3.2	2.00
2	3	4	1	1.0000	6.3	4.00
3	5	6	1	0.8900	7.9	5.00
4	7	8	1	0.8440	8.7	5.50
5	9	10	1	0.7010	12.6	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0172	0.7281	1.4293	0.9958	0.7128	0.8762
1.0130	1.0130	2.0213	0.9917	0.9917	1.2392
1.0109	1.1358	2.2599	0.9896	1.1120	1.3854
1.0098	1.1964	2.3702	0.9886	1.1713	1.4530
1.0046	1.4331	2.8586	0.9835	1.4030	1.7524
QSTD	m=	2.02017	QA	m=	1.26500
	b=	-0.03691		b=	-0.02263
	r=	0.99988		r=	0.99988

Calculations	
Vstd = ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va = ΔVol((Pa-ΔP)/Pa)
Qstd = Vstd/ΔTime	Qa = Va/ΔTime
For subsequent flow rate calculations:	
Qstd = $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa = $1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
 Manufacturer: Sibata LD-3B
 Serial No. 3Y6502
 Equipment Ref: EQ113
 Job Order HK1825889

Standard Equipment:

Standard Equipment: Higher Volume Sampler
 Location & Location ID: AUES office (calibration room)
 Equipment Ref: HVS 018
 Last Calibration Date: 27 February 2018

Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4322	34.1
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4416	32.9
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4811	35.0

Sensitivity Adjustment Scale Setting (Before Calibration) 573 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 573 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9984

Date of Issue 15 March 2018

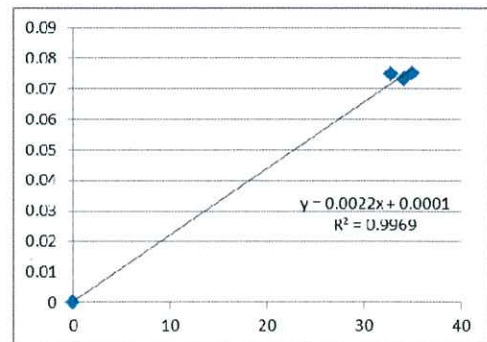

Remarks:

- Strong** Correlation ($R > 0.8$)
 - Factor 0.0022 should be apply for TSP monitoring
- *If $R < 0.5$, repair or re-verification is required for the equipment

Operator : Martin Li Signature :  Date : 15 March 2018

QC Reviewer : Ben Tam Signature :  Date : 15 March 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

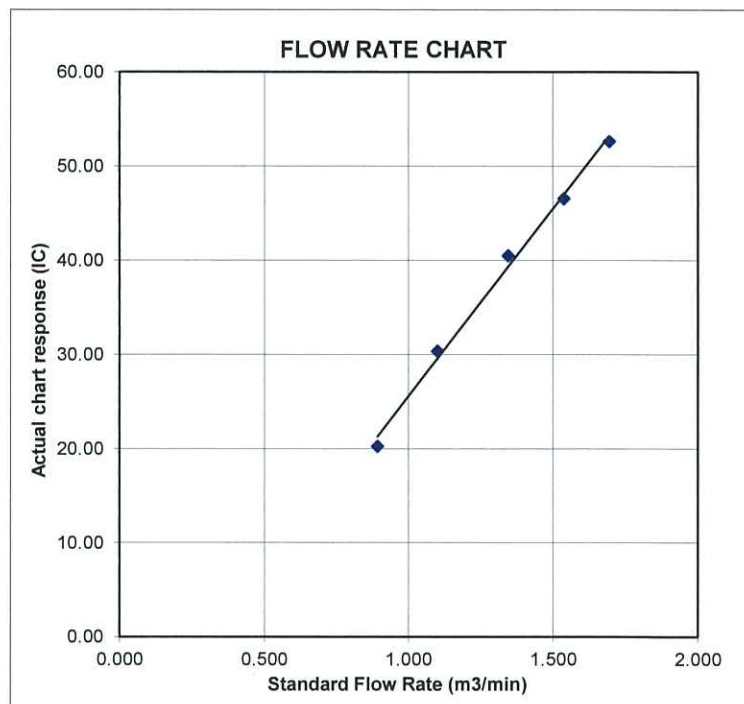

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
 Manufacturer: Sibata LD-3B
 Serial No. 3Y6501
 Equipment Ref: EQ111
 Job Order HK1825888

Standard Equipment:

Standard Equipment: Higher Volume Sampler
 Location & Location ID: AUES office (calibration room)
 Equipment Ref: HVS 018
 Last Calibration Date: 27 February 2018

Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4211	33.3
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4313	32.1
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4771	34.7

Sensitivity Adjustment Scale Setting (Before Calibration) 657 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 656 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9979

Date of Issue 15 March 2018

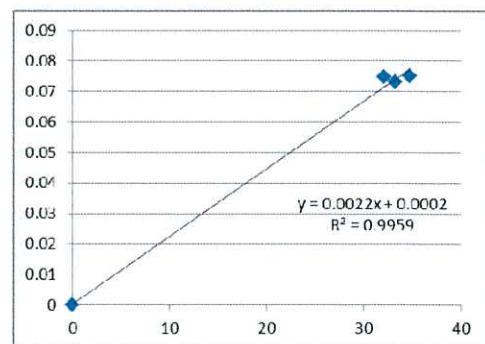

Remarks:

- Strong** Correlation ($R > 0.8$)
 - Factor 0.0022 should be apply for TSP monitoring
- *If $R < 0.5$, repair or re-verification is required for the equipment

Operator : Martin Li Signature :  Date : 15 March 2018

QC Reviewer : Ben Tam Signature :  Date : 15 March 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

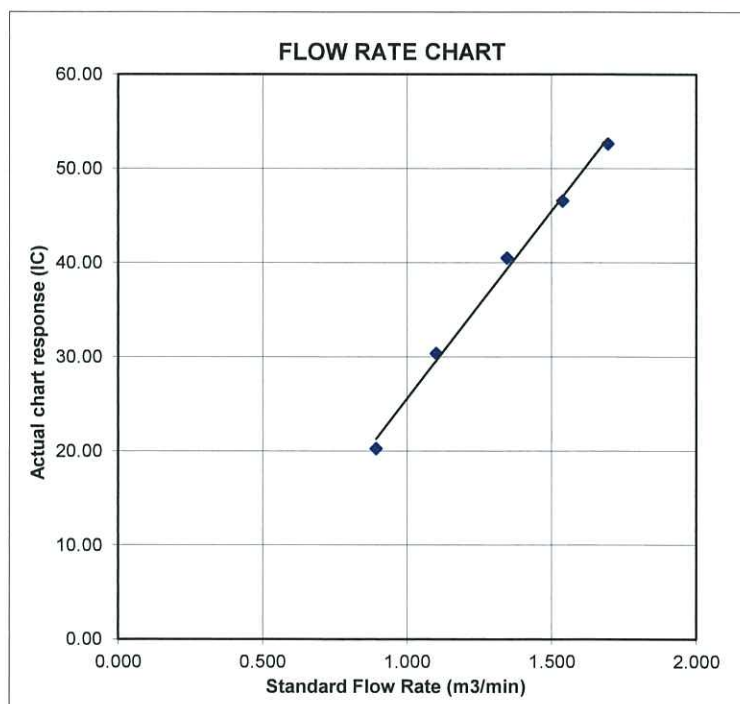

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
 Manufacturer: Sibata LD-3B
 Serial No. 366418
 Equipment Ref: EQ108
 Job Order HK1825887

Standard Equipment:

Standard Equipment: Higher Volume Sampler
 Location & Location ID: AUES office (calibration room)
 Equipment Ref: HVS 018
 Last Calibration Date: 27 February 2018

Equipment Verification Results:

Calibration Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4313	34.1
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4427	32.9
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4626	33.7

Sensitivity Adjustment Scale Setting (Before Calibration) 685 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 685 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9989

Date of Issue 15 March 2018

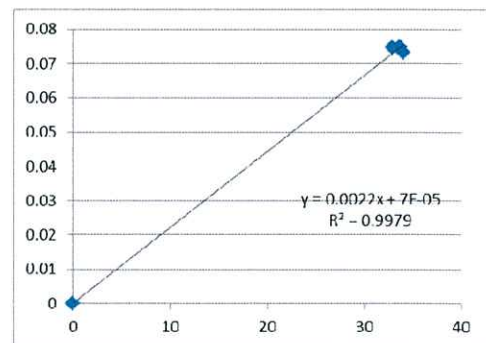

Remarks:

- Strong** Correlation (R>0.8)
 - Factor 0.0022 should be apply for TSP monitoring
- *If R<0.5, repair or re-verification is required for the equipment

Operator : Martin Li Signature : [Signature] Date : 15 March 2018

QC Reviewer : Ben Tam Signature : [Signature] Date : 15 March 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

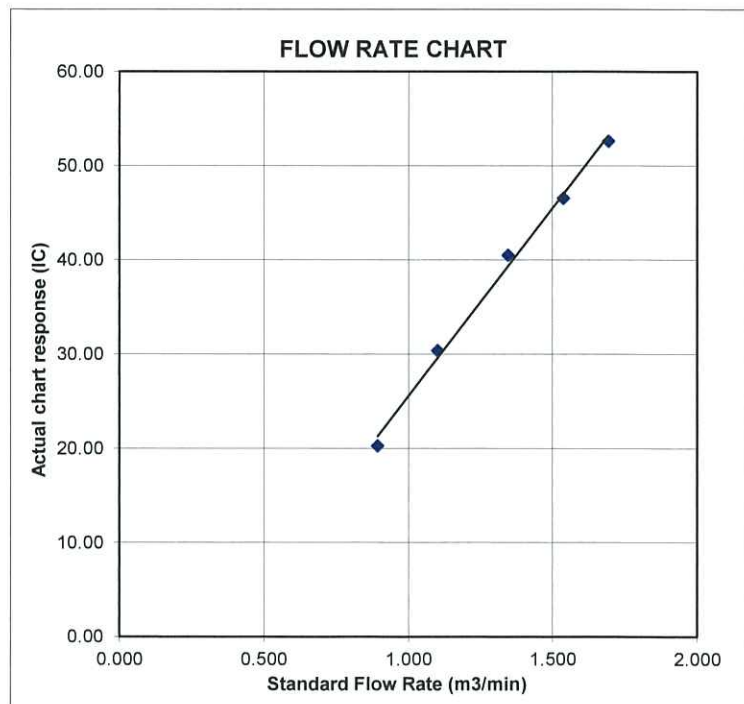

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD-3B
Serial No. 366407
Equipment Ref: EQ107
Job Order HK1825886

Standard Equipment:

Standard Equipment: Higher Volume Sampler
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 27 February 2018

Equipment Verification Results:

Testing Date: 12 & 13 March 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	9:50 ~ 11:57	19.6	1019.0	0.073	4126	32.6
2hr14min	12:05 ~ 14:19	19.6	1019.0	0.075	4414	32.8
2hr17min	9:50 ~ 12:07	20.9	1016.7	0.075	4723	34.4

Sensitivity Adjustment Scale Setting (Before Calibration) 565 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 566 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient (R) 0.9993

Date of Issue 15 March 2018

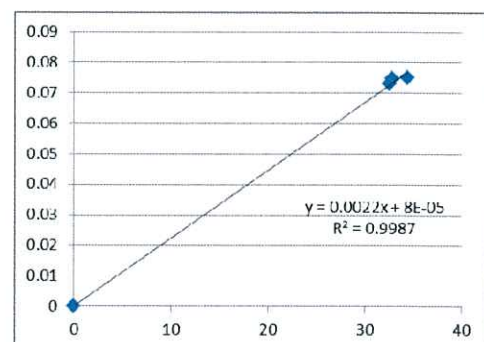

Remarks:

- Strong** Correlation ($R > 0.8$)
 - Factor 0.0022 should be apply for TSP monitoring
- *If $R < 0.5$, repair or re-verification is required for the equipment

Operator : Martin Li Signature : [Signature] Date : 15 March 2018

QC Reviewer : Ben Tam Signature : [Signature] Date : 15 March 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 27-Feb-18
Location ID :	Calibration Room	Next Calibration Date: 27-May-18

CONDITIONS

Sea Level Pressure (hPa)	1017.3	Corrected Pressure (mm Hg)	762.975
Temperature (°C)	19.1	Temperature (K)	292

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.694	52	52.63	Slope = 39.8525 Intercept = -14.3322 Corr. coeff. = 0.9974
13	5.1	5.1	10.2	1.538	46	46.55	
10	3.9	3.9	7.8	1.346	40	40.48	
8	2.6	2.6	5.2	1.101	30	30.36	
5	1.7	1.7	3.4	0.893	20	20.24	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

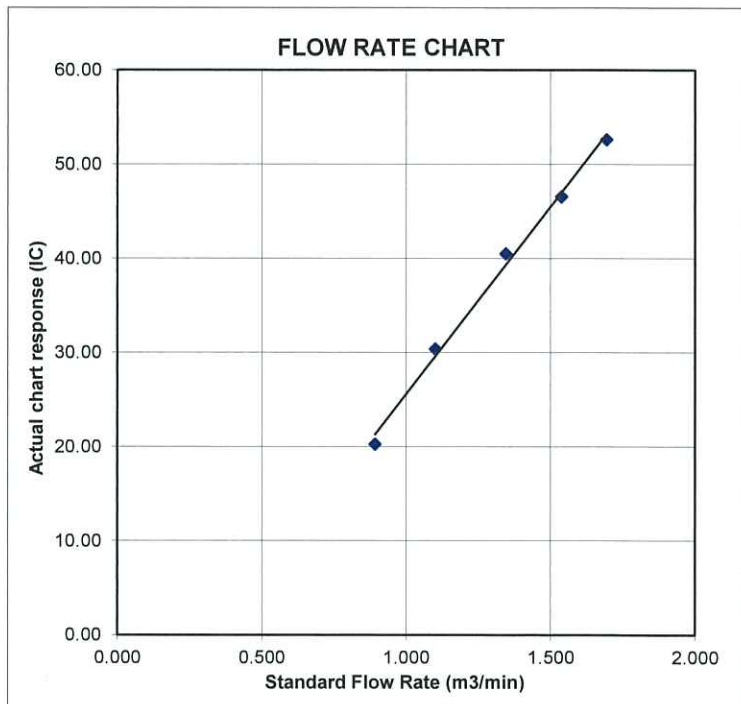



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C183262

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 12 June 2018

Description / 儀器名稱 : Sound Level Meter

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00464681

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C

Relative Humidity / 相對濕度 : (50 ± 25)%

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 18 June 2018

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By


測試



H T Wong
Technical Officer

Certified By

核證



K C Lee
Engineer

Date of Issue

簽發日期

20 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C183262

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	93.6	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	93.6 (Ref.)
				104.00		103.6
				114.00		113.6

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	93.6	Ref.
			Slow			93.6	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C183262

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _A	A	Fast	94.00	63 Hz	67.3	-26.2 ± 1.5
					125 Hz	77.3	-16.1 ± 1.5
					250 Hz	84.9	-8.6 ± 1.4
					500 Hz	90.3	-3.2 ± 1.4
					1 kHz	93.6	Ref.
					2 kHz	94.8	+1.2 ± 1.6
					4 kHz	94.6	+1.0 ± 1.6
					8 kHz	92.5	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.1	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _C	C	Fast	94.00	63 Hz	92.7	-0.8 ± 1.5
					125 Hz	93.3	-0.2 ± 1.5
					250 Hz	93.5	0.0 ± 1.4
					500 Hz	93.6	0.0 ± 1.4
					1 kHz	93.6	Ref.
					2 kHz	93.4	-0.2 ± 1.6
					4 kHz	92.8	-0.8 ± 1.6
					8 kHz	90.6	-3.0 (+2.1 ; -3.1)
					12.5 kHz	87.2	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 07619

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C182473

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 26 April 2018

Description / 儀器名稱 : Sound Level Meter (EQ015)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00142581

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C

Relative Humidity / 相對濕度 : (50 ± 25)%

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 12 May 2018

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試


H T Wong
Technical Officer

Certified By

核證


K C Lee
Engineer

Date of Issue

簽發日期

15 May 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Certificate of Calibration 校正證書

Certificate No. : C183260

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C173864
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C181288

- Test procedure : MA100N.

- Results :

- 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.3	± 0.2

- 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.001	1 kHz ± 1 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



Certificate of Calibration

校正證書

Certificate No. : C182473

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.3	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	94.3 (Ref.)
				104.00		104.3
				114.00		114.3

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.3	Ref.
			Slow			94.3	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C183260

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 12 June 2018

Description / 儀器名稱 : Sound Calibrator (EQ083)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NC-74

Serial No. / 編號 : 34246492

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C

Relative Humidity / 相對濕度 : (50 ± 25)%

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 18 June 2018

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.


The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By
測試


H T Wong
Technical Officer

Certified By
核證


K C Lee
Engineer

Date of Issue
簽發日期

20 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C182473

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _A	A	Fast	94.00	63 Hz	68.0	-26.2 ± 1.5
					125 Hz	78.1	-16.1 ± 1.5
					250 Hz	85.6	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.3	Ref.
					2 kHz	95.5	+1.2 ± 1.6
					4 kHz	95.3	+1.0 ± 1.6
					8 kHz	93.3	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _C	C	Fast	94.00	63 Hz	93.5	-0.8 ± 1.5
					125 Hz	94.1	-0.2 ± 1.5
					250 Hz	94.3	0.0 ± 1.4
					500 Hz	94.3	0.0 ± 1.4
					1 kHz	94.3	Ref.
					2 kHz	94.1	-0.2 ± 1.6
					4 kHz	93.5	-0.8 ± 1.6
					8 kHz	91.4	-3.0 (+2.1 ; -3.1)
					12.5 kHz	87.9	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 06015

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB : 63 Hz - 125 Hz	: ± 0.35 dB
250 Hz - 500 Hz	: ± 0.30 dB
1 kHz	: ± 0.20 dB
2 kHz - 4 kHz	: ± 0.35 dB
8 kHz	: ± 0.45 dB
12.5 kHz	: ± 0.70 dB
104 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Certificate of Calibration 校正證書

Certificate No. : C183082
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867) Date of Receipt / 收件日期 : 28 May 2018
Description / 儀器名稱 : Acoustical Calibrator (EQ081)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 4231
Serial No. / 編號 : 2326408
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^\circ\text{C}$ Relative Humidity / 相對濕度 : $(50 \pm 25)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 9 June 2018


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By : 
測試 : K C Lee
Engineer

Certified By : 
核證 : H C Chan
Engineer

Date of Issue : 11 June 2018
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C183082
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C173864
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C181288

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :
Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1846347
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	27-Aug-2018
		DATE OF ISSUE:	04-Sep-2018

COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	Turbidity
Equipment Type:	Turbidimeter
Brand Name:	Hach
Model No.:	2100Q
Serial No.:	11030C008499
Equipment No.:	—
Date of Calibration:	30 August, 2018

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico
Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1846347
SUB-BATCH: 0
DATE OF ISSUE: 04-Sep-2018
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Turbidimeter
Brand Name: Hach
Model No.: 2100Q
Serial No.: 11030C008499
Equipment No.: --
Date of Calibration: 30 August, 2018

Date of Next Calibration: 30 November, 2018

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.17	--
4	--	N/A
40	41.10	+2.8
80	84.8	+6.0
400	383	-4.3
800	790	-1.3
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

A handwritten signature in black ink, appearing to read 'Chan Siu Ming'.

Mr Chan Siu Ming, Vico
Manager - Inorganic



REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1846345
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	27-Aug-2018
		DATE OF ISSUE:	03-Sep-2018

COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	pH Value and Temperature
Equipment Type:	pH meter
Brand Name:	AZ
Model No.:	8685
Serial No.:	1118396
Equipment No.:	--
Date of Calibration:	30 August, 2018

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Ms. Lin Wai Yu
Assistant Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1846345
SUB-BATCH: 0
DATE OF ISSUE: 03-Sep-2018
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: pH meter
Brand Name: AZ
Model No.: 8685
Serial No.: 1118396
Equipment No.: --
Date of Calibration: 30 August, 2018 **Date of Next Calibration:** 30 November, 2018

PARAMETERS:

pH Value Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	4.0	+0.00
7.0	7.0	+0.00
10.0	9.8	-0.20
	Tolerance Limit (pH unit)	±0.20

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
11.0	11.5	+0.5
22.0	22.0	+0.0
38.5	37.5	-1.0
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu
 Assistant Manager - Inorganic



REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR BEN TAM	WORK ORDER:	HK1840311
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, Kwai Chung, N.T., HONG KONG.	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	20-Jul-2018
		DATE OF ISSUE:	25-Jul-2018

COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	Dissolved Oxygen and Temperature
Equipment Type:	Dissolved Oxygen Meter
Brand Name:	YSI
Model No.:	Pro 20
Serial No.:	12C100570
Equipment No.:	--
Date of Calibration:	25 July, 2018

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vico
Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as listed in the HOKLAS Directory of Accredited Laboratories within the test category of
此實驗所符合ISO / IEC 17025 : 2005 –《測試及校正實驗所能力的通用規定》所訂的要求，獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (see joint IAF-ILAC-ISO Communiqué).
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS 066**
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



Appendix G

Event and Action Plan

Event and Action Plan for Air Quality

Event	ET	IEC	ER	Action Contractor
Action Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Monitor the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Monitor the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented;	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not
	and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	the ER accordingly; 5. Monitor the implementation of remedial measures.	5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event and Action Plan for Construction Noise

Event		ET	IEC	ER	Action Contractor
Action Level	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures.	1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals.	
Limit Level	1. Inform IEC, ER, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated.	

Event and Action Plan for Water Quality

EVENT	ACTION CONTRACTOR			
	ET	IEC	ER	
Action level being exceeded by one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Identify reasons for non-compliance and sources of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures.
Action Level being exceeded by more than two consecutive sampling days	<ol style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Identify reasons for non-compliance and sources of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 2 working days; Implement the agreed mitigation measures.
Limit Level being exceeded by one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Identify reasons for non-compliance and sources of impact; Inform IEC, Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level. 	<ol style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures.
Limit level being exceeded by more than one consecutive sampling days	<ol style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Identify reasons for non-compliance and sources of impact; Inform IEC, Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days. 	<ol style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit Level. 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the ER, to slow down or to stop all or part of the construction activities.

Appendix H

Impact Monitoring Schedule

Impact Monitoring Schedule for Reporting Period – September 2018

Date		Dust Monitoring		Noise Monitoring	Water Quality
		1-hour TSP	24-hour TSP		
Sat	1-Sep-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Sun	2-Sep-18				
Mon	3-Sep-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	All Water Quality Monitoring Locations
Tue	4-Sep-18				
Wed	5-Sep-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	All Water Quality Monitoring Locations
Thu	6-Sep-18				
Fri	7-Sep-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Sat	8-Sep-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b		
Sun	9-Sep-18				
Mon	10-Sep-18				
Tue	11-Sep-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	All Water Quality Monitoring Locations
Wed	12-Sep-18				
Thu	13-Sep-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Fri	14-Sep-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	
Sat	15-Sep-18				All Water Quality Monitoring Locations
Sun	16-Sep-18				
Mon	17-Sep-18	AM9b		NM8, NM9 & NM10	
Tue	18-Sep-18	AM1c, AM2 & AM3*		NM1, NM2a*	All Water Quality Monitoring Locations*
Wed	19-Sep-18		AM4b, AM5, AM6, AM7b & AM8		
Thu	20-Sep-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	All Water Quality Monitoring Locations
Fri	21-Sep-18				
Sat	22-Sep-18	AM1c, AM2, AM3 & AM9b			All Water Quality Monitoring Locations
Sun	23-Sep-18				
Mon	24-Sep-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Tue	25-Sep-18				
Wed	26-Sep-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	
Thu	27-Sep-18				All Water Quality Monitoring Locations
Fri	28-Sep-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	
Sat	29-Sep-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Sun	30-Sep-18				

Remark:* Since the access road to all water quality monitoring locations, 1-hour TSP monitoring location at AM1c, AM2 & AM3 and Noise monitoring location at NM1 and NM2 were blocked by fell trees due to Typhoon Mangkhut, the monitoring events in these locations scheduled on 17 Sep 18 were cancelled and were rescheduled to 18 Sep 18.

	Monitoring Day
	Sunday or Public Holiday

Impact Monitoring Schedule for next Reporting Period – October 2018

Date		Dust Monitoring		Noise Monitoring	Water Quality
		1-hour TSP	24-hour TSP		
Mon	1-Oct-18				
Tue	2-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	All Water Quality Monitoring Locations
Wed	3-Oct-18				
Thu	4-Oct-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	All Water Quality Monitoring Locations
Fri	5-Oct-18		AM4b, AM5, AM6, AM7b & AM8		
Sat	6-Oct-18				All Water Quality Monitoring Locations
Sun	7-Oct-18				
Mon	8-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	
Tue	9-Oct-18				All Water Quality Monitoring Locations
Wed	10-Oct-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	
Thu	11-Oct-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Fri	12-Oct-18				
Sat	13-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b		All Water Quality Monitoring Locations
Sun	14-Oct-18				
Mon	15-Oct-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	
Tue	16-Oct-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Wed	17-Oct-18				
Thu	18-Oct-18				All Water Quality Monitoring Locations
Fri	19-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	
Sat	20-Oct-18	AM1c, AM2, AM3 & AM9b			All Water Quality Monitoring Locations
Sun	21-Oct-18				
Mon	22-Oct-18		AM4b, AM5, AM6, AM7b & AM8		
Tue	23-Oct-18				All Water Quality Monitoring Locations
Wed	24-Oct-18				
Thu	25-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	All Water Quality Monitoring Locations
Fri	26-Oct-18	AM1c, AM2, AM3 & AM9b		NM1, NM2a, NM8, NM9 & NM10	
Sat	27-Oct-18		AM4b, AM5, AM6, AM7b & AM8		All Water Quality Monitoring Locations
Sun	28-Oct-18				
Mon	29-Oct-18				All Water Quality Monitoring Locations
Tue	30-Oct-18				
Wed	31-Oct-18	AM4b, AM5, AM6, AM7b & AM8	AM1c, AM2, AM3 & AM9b	NM3, NM4, NM5, NM6 & NM7	All Water Quality Monitoring Locations

	Monitoring Day
	Sunday or Public Holiday

Appendix I

Database of Monitoring Result

24-hour TSP Monitoring Data

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-HR TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
AM1c – Open Area, Tsung Yuen Ha Village No.63															
3-Sep-18	22843	14946.52	14970.52	1440.00	23	23	23.0	27.7	1006.9	0.83	1190	2.6685	2.7095	0.0410	34
8-Sep-18	22851	14970.52	14994.52	1440.00	25	25	25.0	29.6	1008.6	0.90	1289	2.6671	2.7423	0.0752	58
14-Sep-18	23086	14994.52	15018.52	1440.00	25	25	25.0	28.8	1009.2	0.90	1291	2.6616	2.7246	0.0630	49
20-Sep-18	23105	15018.52	15042.52	1440.00	20	20	20.0	29	1011	0.72	1037	2.6791	2.8256	0.1465	141
26-Sep-18	23137	15042.52	15066.52	1440.00	22	22	22.0	26.8	1009.6	0.78	1128	2.6607	2.6836	0.0229	20
AM2 - Village House near Lin Ma Hang Road															
3-Sep-18	22844	10566.17	10589.80	1417.80	25	25	25.0	27.7	1006.9	0.81	1149	2.6612	2.7134	0.0522	45
8-Sep-18	22850	10589.80	10613.57	1426.20	28	28	28.0	29.6	1008.6	0.90	1286	2.6617	2.7984	0.1367	106
14-Sep-18	23085	10613.57	10637.22	1419.00	38	38	38.0	28.8	1009.2	1.22	1725	2.6711	2.9124	0.2413	140
20-Sep-18	23106	10637.22	10660.97	1425.00	38	38	38.0	29	1011	1.22	1734	2.6865	2.8888	0.2023	117
26-Sep-18	23102	10660.97	10684.74	1426.20	42	42	42.0	26.8	1009.6	1.35	1919	2.6790	2.8242	0.1452	76
AM3 - Ta Kwu Ling Fire Service Station of Ta Kwu Ling Village															
3-Sep-18	22824	11685.31	11709.30	1439.40	34	34	34.0	27.7	1006.9	1.06	1529	2.6820	2.7721	0.0901	59
8-Sep-18	22849	11709.30	11733.31	1440.60	35	36	35.5	29.6	1008.6	1.12	1606	2.6607	2.8894	0.2287	142
14-Sep-18	23084	11733.31	11757.31	1440.00	33	34	33.5	28.8	1009.2	1.04	1502	2.6609	2.8266	0.1657	110
20-Sep-18	23107	11757.31	11781.32	1440.60	26	26	26.0	29	1011	0.77	1102	2.6831	2.7107	0.0276	25
26-Sep-18	23103	11781.32	11805.32	1440.00	22	22	22.0	26.8	1009.6	0.62	891	2.7009	2.7202	0.0193	22
AM4b - House no. 10B1 Nga Yiu Ha Village															
1-Sep-18	22823	13672.56	13696.10	1412.40	38	38	38.0	26.3	1009.9	1.15	1627	2.6684	2.7159	0.0475	29
7-Sep-18	22846	13696.10	13719.95	1431.00	36	36	36.0	29.4	1006.3	1.08	1546	2.6556	2.7527	0.0971	63
13-Sep-18	23081	13719.95	13743.95	1440.00	36	36	36.0	27.7	1009.4	1.09	1563	2.6916	2.7339	0.0423	27
19-Sep-18	23088	13743.95	13767.95	1440.00	38	38	38.0	28.6	1012.7	1.15	1655	2.6727	2.7851	0.1124	68
24-Sep-18	23100	13767.95	13791.93	1438.80	38	38	38.0	27	1011.1	1.15	1657	2.6961	2.7670	0.0709	43
29-Sep-18	23139	13791.93	13815.93	1440.00	36	38	37.0	27.4	1008.9	1.12	1609	2.6855	2.8595	0.1740	108
AM5a - Ping Yeung Village House															
1-Sep-18	22821	12520.36	12544.00	1418.40	30	30	30.0	26.3	1009.9	1.32	1875	2.6677	2.7173	0.0496	26
7-Sep-18	22847	12544.00	12567.78	1426.80	42	42	42.0	29.4	1006.3	1.64	2337	2.6707	2.7763	0.1056	45
13-Sep-18	23082	12567.78	12591.80	1441.20	30	30	30.0	27.7	1009.4	1.32	1903	2.6802	2.7682	0.0880	46
19-Sep-18	23089	12591.80	12615.50	1422.00	40	40	40.0	28.6	1012.7	1.59	2260	2.6777	2.8007	0.1230	54
24-Sep-18	23109	12615.50	12639.20	1422.00	42	42	42.0	27	1011.1	1.64	2339	2.6740	2.7620	0.0880	38

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-HR TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
29-Sep-18	23140	12639.20	12662.86	1419.60	42	42	42.0	27.4	1008.9	1.64	2332	2.6671	2.9792	0.3121	134
AM6 - Wo Keng Shan Village House															
1-Sep-18	22822	10117.56	10141.57	1440.60	25	25	25.0	26.3	1009.9	0.80	1153	2.6569	2.6864	0.0295	26
7-Sep-18	22848	10141.57	10165.58	1440.60	30	30	30.0	29.4	1006.3	0.96	1377	2.6782	2.7800	0.1018	74
13-Sep-18	23083	10165.58	10189.58	1440.00	30	30	30.0	27.7	1009.4	0.96	1382	2.6870	2.7855	0.0985	71
19-Sep-18	23104	10189.58	10213.60	1441.20	30	30	30.0	28.6	1012.7	0.96	1384	2.6936	2.7999	0.1063	77
24-Sep-18	23108	10213.60	10237.60	1440.00	32	32	32.0	27.0	1011.1	1.03	1479	2.6832	2.7556	0.0724	49
29-Sep-18	23141	10237.60	10261.61	1440.60	34	34	34.0	27.4	1008.9	1.09	1570	2.6499	2.8456	0.1957	125
AM7b - Loi Tung Village House															
1-Sep-18	22827	19164.28	19188.29	1440.60	32	32	32.0	28.7	1006.2	1.07	1540	2.6857	2.7233	0.0376	24
7-Sep-18	23091	19188.29	19212.29	1440.00	38	38	38.0	28.1	1007.4	1.23	1768	2.6727	2.7733	0.1006	57
13-Sep-18	22854	19212.29	19236.30	1440.60	40	40	40.0	27.7	1009.4	1.28	1847	2.6545	2.7545	0.1000	54
19-Sep-18	22800	19236.30	19260.30	1440.00	38	38	38.0	28.6	1012.7	1.23	1771	2.6768	2.8348	0.1580	89
24-Sep-18	23124	19260.30	19284.31	1440.60	38	38	38.0	27	1011.1	1.23	1774	2.6559	2.7195	0.0636	36
29-Sep-18	23069	19284.31	19308.31	1440.00	42	42	42.0	26.8	1011.8	1.34	1926	2.6713	2.8847	0.2134	111
AM8 - Po Kat Tsai Village No. 4															
1-Sep-18	22842	13061.16	13085.17	1440.60	32	32	32.0	28.7	1006.2	1.12	1616	2.6694	2.7040	0.0346	21
7-Sep-18	23092	13085.17	13109.18	1440.60	34	34	34.0	28.1	1007.4	1.17	1682	2.6826	2.7425	0.0599	36
13-Sep-18	23080	13109.18	13133.18	1440.00	36	37	36.5	27.7	1009.4	1.23	1765	2.6801	2.7192	0.0391	22
19-Sep-18	23065	13133.18	13157.00	1429.20	42	42	42.0	28.6	1012.7	1.35	1930	2.6765	2.8850	0.2085	108
24-Sep-18	23101	13157.00	13180.55	1413.00	38	40	39.0	27	1011.1	1.28	1814	2.6922	2.7344	0.0422	23
29-Sep-18	23070	13180.55	13204.55	1440.00	38	38	38.0	26.8	1011.8	1.26	1817	2.6820	2.8019	0.1199	66
AM9b - Nam Wa Po Village House No. 80															
3-Sep-18	23079	20440.64	20464.64	1440.00	32	32	32.0	28.5	1006.6	1.10	1586	2.6790	2.7206	0.0416	26
8-Sep-18	22852	20464.64	20488.65	1440.60	32	32	32.0	29.6	1008.6	1.10	1586	2.6580	2.7384	0.0804	51
14-Sep-18	22837	20488.65	20512.65	1440.00	32	32	32.0	27.9	1008.6	1.10	1588	2.6692	2.7394	0.0702	44
20-Sep-18	23146	20512.65	20536.65	1440.00	32	32	32.0	29	1011	1.10	1588	2.6692	2.7425	0.0733	46
26-Sep-18	23138	20536.65	20560.65	1440.00	25	25	25.0	26.8	1009.6	0.92	1318	2.6806	2.7433	0.0627	48

Construction Noise Monitoring Results, dB(A)

Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 rd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq ₃₀	façade correction
NM1 - Tsung Yuen Ha Village House No. 63																					
5-Sep-18	9:42	59.8	61.6	54.1	60.5	62.6	55.1	57.1	58.8	53.7	58.4	59.6	54.1	59.0	60.9	54.3	61.2	62.6	55.0	60	NA
11-Sep-18	9:49	56.6	58.4	52.3	56.2	58.4	52.4	58.7	60.8	52.0	59.3	61.6	52.2	58.5	62.5	53.3	55.6	59.5	53.3	58	NA
18-Sep-18#	9:32	53.7	55.3	51.7	53.5	55.1	51.5	53.9	55.8	51.7	54.6	56.1	52.2	55.6	56.2	52.3	54.9	55.8	51.8	54	NA
28-Sep-18	9:40	55.8	58.4	53.1	55.3	57.4	53.7	54.8	57.7	53.8	54.9	58.4	53.4	57.5	60.5	53.6	54.4	56.5	53.9	56	NA
NM2a - Village House near Lin Ma Hang Road																					
5-Sep-18	10:27	72.6	68.9	53.4	62.6	60.4	52.4	64.5	67.3	54.8	63.0	65.7	52.0	61.2	63.1	51.2	59.0	60.1	52.0	67	70
11-Sep-18	10:34	70.9	68.1	53.4	63.2	65.1	52.8	62.4	64.7	52.6	60.5	62.1	52.0	63.6	65.3	53.0	62.2	64.3	53.3	65	68
18-Sep-18#	10:11	70.9	55.8	48.4	55.8	57.7	48.2	70.0	62.8	48.1	59.2	63.1	49.8	56.0	59.1	48.7	58.4	61.7	49.7	66	69
28-Sep-18	10:22	69.6	65.3	49.4	60.4	63.8	50.1	68.6	63.7	48.2	64.9	62.8	48.3	63.0	62.9	47.3	61.5	61.9	47.3	66	69
NM3 - Ping Yeung Village House																					
3-Sep-18	10:11	57.0	59.5	52.5	57.6	60.5	51.5	56.6	59.5	51.5	58.2	61.5	51.5	57.7	61.0	52.0	57.7	60.0	53.0	57	NA
14-Sep-18	10:03	63.6	66.9	53.3	63.1	66.0	54.8	63.0	65.6	54.8	62.3	66.0	53.7	63.5	66.8	52.8	62.2	65.1	53.0	63	NA
20-Sep-18	10:38	61.3	64.2	52.2	56.5	57.5	51.7	57.6	57.6	51.6	59.1	59.9	51.5	59.1	59.8	51.6	59.0	60.7	51.6	59	NA
26-Sep-18	13:12	60.9	65.2	52.8	59.4	64.1	51.9	58.2	66.2	50.8	54.6	59.4	50.1	55.2	59.8	49.8	54.2	58.4	49.6	58	NA
NM4 - Wo Keng Shan Village House																					
3-Sep-18	11:01	58.6	58.5	53.0	56.6	58.0	53.5	57.7	60.5	51.0	57.6	60.0	50.5	56.1	58.5	50.5	56.5	59.0	52.0	57	NA
14-Sep-18	10:37	60.7	64.0	51.8	60.8	63.4	54.0	61.7	65.2	53.9	61.9	65.3	52.6	61.2	64.3	54.0	65.3	68.3	57.2	62	NA
20-Sep-18	11:26	64.8	63.4	52.4	64.1	61.8	51.5	61.8	61.7	51.4	60.2	60.7	51.4	61.3	60.5	51.0	60.3	59.2	51.2	62	NA
26-Sep-18	14:11	55.9	59.2	50.1	54.2	60.1	51.1	56.8	60.8	50.8	62.4	66.1	58.2	54.9	59.2	50.8	55.2	60.2	51.2	58	NA
NM5 - Ping Yeung Village House																					
3-Sep-18	10:46	60.4	62.1	49.9	59.1	62.7	48.5	57.6	60.6	51.4	59.2	62.4	47.8	58.9	62.1	50.5	58.0	61.3	49.1	59	NA
14-Sep-18	9:43	55.8	57.5	53.0	55.6	58.5	52.0	55.4	58.5	48.5	52.7	55.0	50.0	54.3	57.0	49.0	54.6	56.0	49.0	55	NA
20-Sep-18	13:10	56.8	58.0	54.2	55.9	57.2	54.8	58.2	59.8	56.2	57.1	59.4	54.4	56.8	58.0	54.9	56.9	58.0	53.6	57	NA
26-Sep-18	10:29	55.9	58.5	50.5	55.2	58.5	48.5	57.3	60.0	60.0	56.5	59.5	48.5	55.5	58.0	50.0	55.8	59.0	48.0	56	NA
NM6 - Tai Tong Wu Village House 2																					
3-Sep-18	9:34	59.1	61.9	54.5	60.5	62.8	56.7	63.2	67.6	57.0	58.9	61.0	55.4	60.4	62.4	57.0	59.4	61.5	55.3	61	NA
14-Sep-18	10:32	61.1	53.0	51.0	56.5	58.0	54.0	56.1	57.5	54.0	58.2	59.0	55.0	57.2	58.5	55.0	55.8	57.0	54.0	58	NA
20-Sep-18	10:17	55.9	57.1	53.7	56.1	57.0	54.5	56.2	57.6	54.5	56.4	58.7	53.1	58.5	60.0	53.9	61.8	66.8	53.2	58	NA
26-Sep-18	9:25	59.3	58.0	48.5	56.1	59.0	48.0	57.2	60.0	49.0	57.5	60.5	50.5	57.8	59.5	53.5	58.2	59.0	57.0	58	NA
NM7 - Po Kat Tsai Village																					
3-Sep-18	13:05	61.5	63.7	58.3	61.6	63.9	58.5	61.3	63.3	58.1	62.4	63.6	58.2	61.8	63.7	59.0	65.8	70.1	59.3	63	NA

Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 rd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq30	façade correction
14-Sep-18	13:12	62.0	63.0	61.0	61.9	62.5	61.0	62.6	64.0	61.0	68.0	71.5	60.0	64.0	66.0	61.0	62.2	63.0	61.0	64	NA
20-Sep-18	13:10	65.9	64.0	53.5	61.1	63.5	53.5	60.1	63.0	53.5	61.1	64.0	54.5	61.4	64.5	54.5	63.3	66.5	55.5	63	NA
26-Sep-18	13:22	65.9	67.0	62.5	65.7	67.0	62.0	66.2	67.5	63.0	66.1	67.5	62.5	65.8	67.0	62.0	66.2	67.5	62.5	66	NA
NM8 - Village House, Tong Hang																					
5-Sep-18	10:55	56.7	58.1	55	58.2	61.6	55.1	60.5	62.7	55.3	59.6	62.5	55.5	62.2	64.5	58.1	61.4	63.6	56	60	NA
11-Sep-18	10:53	56	57.3	52.8	56.1	57.9	52.3	54.1	55.7	51.7	55	56.7	52.6	55.5	57.1	52.5	57	57.3	52.8	56	NA
17-Sep-18	15:23	66.9	69.6	52.5	66	65.1	50.7	55.6	58.3	49.7	58.9	58.3	48.6	54.7	56.4	48.6	56	58	48.7	63	NA
28-Sep-18	10:59	57	59.5	51	57.6	60	52.5	55.6	58	51	55.1	57.5	50.5	55.6	58.5	50	54.6	57	49	56	NA
NM9 - Village House, Kiu Tau Village																					
5-Sep-18	10:14	61.3	62.5	59.5	62.3	63.4	60.6	62.6	63.9	60.8	58.3	60.0	55.4	58.9	60.2	55.0	59.3	61.8	55.3	61	NA
11-Sep-18	10:07	58.6	60.3	55.9	57.9	59.1	56.3	58.7	60.4	56.6	57.6	58.6	56.4	59.3	61.0	56.3	59.6	61.7	57.1	59	NA
17-Sep-18	14:27	48.4	51.1	39	49.9	52.9	39.5	56.1	59.1	38.8	52.9	54	39.9	57.6	61.5	40.9	57.7	59.9	46.8	55	NA
28-Sep-18	10:04	57.8	61.0	51.5	53.4	56.5	50.0	57.0	60.0	51.0	60.4	63.0	54.0	56.3	59.0	51.0	58.0	60.5	52.5	58	NA
NM10 - Nam Wa Po Village House No. 80																					
5-Sep-18	9:33	61.2	61.8	59.6	62.4	61.5	59.1	61.0	62.1	58.5	63.2	64.0	60.4	62.7	64.4	60.7	61.8	63.6	59.9	62	65
11-Sep-18	9:19	61.0	62.7	58.8	60.8	62.3	59.1	61.2	62.8	59.1	61.0	62.5	59.0	60.5	61.7	58.7	60.6	62.2	58.7	61	64
17-Sep-18	13:33	55.6	57.6	46.6	59	59.4	49	63	58.7	47.6	59.3	62.1	47.4	55.9	57.4	43.9	55.2	57.4	44.9	59	62
28-Sep-18	9:12	56.8	58.5	54.0	58.8	59.0	54.5	57.9	59.5	55.0	57.3	59.0	54.5	57.5	59.5	55.0	57.0	59.0	53.5	58	61

^(#) Since the access road to noise monitoring locations NM1 and NM2 were blocked by fallen trees due to Typhoon Mangkhut, the monitoring event in these locations scheduled on 17 Sep 18 was cancelled and rescheduled to 18 Sep 18.

Water Quality Monitoring Data for Contract 6 and SS C505

Date	1-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:10	0.35	25.9	25.9	7.43	7.5	92.1	92.2	45.7	45.9	6.8	6.8	44	43.5
			25.9		7.48		92.2		46.1		6.8		43	
WM1	10:00	0.35	26.1	26.1	7.7	7.7	95.0	95.1	50.2	50.7	6.8	6.8	51	50.5
			26.1		7.71		95.2		51.1		6.8		50	

Date	3-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:10	0.30	26.5	26.5	7.44	7.5	92.3	92.8	34.2	33.2	6.9	6.9	34	34.5
			26.5		7.48		93.2		32.2		6.9		35	
WM1	10:00	0.25	26.6	26.6	7.76	7.8	95.9	95.9	29.5	29.7	7	7.0	22	22.0
			26.6		7.75		95.9		29.8		7		22	

Date	5-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:05	0.25	28.3	28.3	6.44	6.4	83.0	82.4	16.7	16.8	7.6	7.6	11	11.5
			28.3		6.33		81.8		16.8		7.6		12	
WM1	10:00	0.25	27.6	27.6	6.22	6.2	79.9	79.1	18.0	17.9	9.3	9.3	20	19.5
			27.6		6.09		78.2		17.8		9.3		19	

Date	7-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:25	0.25	28.7	28.7	6.6	6.6	82.4	82.8	12.4	12.4	7.9	7.9	7	7.0
			28.7		6.63		83.1		12.4		7.9		7	
WM1	10:15	0.25	30.6	30.6	6.56	6.5	72.1	72.6	14.3	14.4	8	8.0	13	13.0
			30.6		6.51		73.1		14.5		8		13	

Date	11-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:25	0.30	26.4	26.4	7.82	7.9	90.1	91.0	13.8	13.7	9	9.0	6	6.0
			26.4		7.9		91.9		13.5		9		6	
WM1	10:15	0.22	29.3	29.3	7.82	7.8	80.9	81.5	17.8	17.5	9.2	9.2	11	11.0
			29.3		7.83		82.1		17.2		9.2		11	

Date	13-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:20	0.25	26.3	26.3	6.82	6.5	87.8	84.6	11.2	11.3	8.3	8.3	9	9.0
			26.3		6.26		81.4		11.4		8.3		9	
WM1	10:10	0.22	27.8	27.8	7.03	7.1	91.7	91.8	42.6	41.7	8.3	8.3	50	49.5
			27.8		7.07		91.9		40.7		8.3		49	

Date	15-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:15	0.25	27.4	27.4	6.2	6.2	82.0	81.5	9.8	9.8	7.9	7.9	9	9.0
			27.4		6.19		81.0		9.8		7.9		9	
WM1	10:05	0.18	31.9	31.9	6.99	7.0	89.9	90.2	16.8	16.6	7.7	7.7	50	50.0
			31.9		7.04		90.4		16.4		7.7		50	

Date	18-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	9:50	0.30	26.8	26.8	6.82	6.8	78.5	78.3	16.9	17.0	7.8	7.8	5	5.5
			26.8		6.81		78.0		17.0		7.8		6	
WM1	9:40	0.25	29.1	29.1	7.05	7.3	82.1	82.5	18.1	17.4	7.5	7.5	21	21.5
			29.1		7.58		82.8		16.6		7.5		22	

Date	20-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:40	0.25	28.4	28.4	6.96	6.9	81.1	80.6	12.9	13.0	7.8	7.8	10	10.0
			28.4		6.74		80.1		13.1		7.8		10	
WM1	10:20	0.22	27.2	27.2	6.99	6.9	83.4	83.2	12.8	12.6	7.7	7.7	11	11.0
			27.2		6.87		83.0		12.4		7.7		11	

Date	22-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:35	0.25	27	27.0	7.39	7.4	87.7	88.2	10.8	10.8	7.9	7.9	7	7.5
			27		7.38		88.6		10.8		7.9		8	
WM1	10:20	0.22	26.8	26.8	8	8.3	92.1	91.1	12.6	12.7	7.8	7.8	13	12.5
			26.8		8.5		90.1		12.7		7.8		12	

Date	24-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:50	0.20	27	27.0	6.92	6.9	85.5	85.2	10.6	10.8	7.7	7.7	8	7.0
			27		6.91		84.9		10.9		7.7		6	
WM1	10:35	2.50	27.4	27.4	7.57	7.6	91.1	91.6	11.9	11.8	7.7	7.7	9	9.5
			27.4		7.6		92.0		11.7		7.7		10	

Date	27-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:15	0.30	26.7	26.7	6.94	7.0	86.8	87.0	15.8	15.4	6.65	6.7	9	9.5
			26.7		6.97		87.1		15.0		6.65		10	
WM1	10:05	0.20	26.5	26.5	5.45	5.5	68.0	68.1	20.6	20.4	7.23	7.2	12	13.0
			26.5		5.47		68.1		20.1		7.23		14	

Date	29-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM1-C	10:10	0.30	25.1	25.1	7.29	7.3	88.3	88.5	15.0	15.5	7.54	7.5	16	16.5
			25.1		7.32		88.7		15.9		7.54		17	
WM1	10:00	0.20	24.8	24.8	6.15	6.2	74.0	74.4	16.6	16.8	8.43	46.2	14	13.0
			24.8		6.21		74.8		16.9		84		12	

Water Quality Monitoring Data for Contract 2 and 3

Date		1-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)		
WM4-CA	11:35	0.25	24.9	24.9	8.04	8.0	97.2	97.3	282.0	287.0	6.9	6.9	165	163.5	
			24.9		8.05		97.3		292.0		6.9				
WM4-CB	11:40	0.50	25.6	25.6	7.4	7.4	90.4	90.7	223.0	219.5	6.8	6.8	154	153.0	
			25.6		7.43		90.9		216.0		6.8				
WM4	11:25	0.35	25.5	25.5	7.49	7.5	91.4	91.9	246.0	244.5	6.9	6.9	190	188.5	
			25.5		7.53		92.3		243.0		6.9				

Date		3-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)		
WM4-CA	11:55	0.22	25.7	25.7	9.75	9.6	129.7	127.2	overrange	over range	7.1	7.1	740	744.0	
			25.7		9.54		124.6		overrange		7.1		748		
WM4-CB	12:00	0.30	27.3	27.3	7.18	7.2	92.7	93.0	284.0	281.5	6.9	6.9	177	177.0	
			27.3		7.22		93.2		279.0		6.9		177		
WM4	11:45	0.25	26.8	26.8	7.27	7.3	90.6	90.7	593.0	595.0	6.9	6.9	567	564.5	
			26.8		7.27		90.8		597.0		6.9		562		

Date		5-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)		
WM4-CA	11:45	0.20	32.9	32.9	5.2	5.2	71.9	71.6	6.9	6.6	9.1	9.1	3	3.0	
			32.9		5.16		71.2		6.4		9.1		3		
WM4-CB	12:00	0.25	30.1	30.1	5.73	5.7	76.5	76.0	9.5	9.3	8.7	8.7	8	8.0	
			30.1		5.65		75.4		9.2		8.7		8		
WM4	11:40	0.20	32.7	32.7	5.31	5.3	73.4	73.5	19.9	20.4	9.1	9.1	12	12.5	
			32.7		5.33		73.5		20.8		9.1		13		

Date		7-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)		
WM4-CA	11:55	0.20	29.5	29.5	7.58	7.6	89.7	89.8	4.0	3.9	7.6	7.6	5	5.5	
			29.5		7.57		89.9		3.9		7.6		6		
WM4-CB	12:00	0.24	29.6	29.6	7.45	7.5	80.4	81.3	8.5	8.4	7.4	7.4	2	2.5	
			29.6		7.6		82.1		8.4		7.4		3		
WM4	11:45	0.20	29.6	29.6	7.71	7.7	83.0	83.0	16.9	16.9	7.7	7.7	16	16.0	
			29.6		7.7		83.0		16.8		7.7		16		

Date		11-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)		
WM4-CA	11:45	0.20	28.3	28.3	7.45	7.5	86.6	87.4	4.9	4.8	9.5	9.5	2	2.5	
			28.3		7.56		88.1		4.6		9.5		3		
WM4-CB	12:00	0.25	29.7	29.7	7.1	7.2	83.1	83.6	13.9	13.8	8.3	8.3	11	11.5	
			29.7		7.21		84.1		13.6		8.3		12		
WM4	11:40	0.20	28	28.0	7.57	7.6	87.3	87.5	14.8	14.5	9.2	9.2	12	12.5	
			28		7.59		87.7		14.1		9.2		13		

Date	13-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	12:00	0.16	26.3	26.3	8.26	8.3	99.9	99.9	4.9	5.1	8.2	8.2	4	4.0
			26.3		8.24		99.9		5.4		8.2		4	
WM4-CB	12:10	0.25	27.5	27.5	8.88	8.9	94.8	89.6	15.7	15.5	7.8	7.8	12	12.0
			27.5		8.83		84.4		15.2		7.8		12	
WM4	11:55	0.20	26.7	26.7	8.22	8.2	90.5	90.5	31.6	28.7	8	8.0	28	27.5
			26.7		8.2		90.4		25.7		8		27	

Date	15-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	11:40	0.15	29	29.0	7.26	7.3	88.2	88.3	2.8	2.7	8.4	8.4	5	5.5
			29		7.25		88.4		2.5		8.4		6	
WM4-CB	11:50	0.25	30.5	30.5	7.32	7.4	87.3	87.7	4.5	4.1	8	8.0	13	12.5
			30.5		7.38		88.0		3.6		8		12	
WM4	11:35	0.20	28.8	28.8	7.47	7.5	87.7	87.6	16.7	16.3	8.6	8.6	23	23.5
			28.8		7.47		87.5		15.9		8.6		24	

Date	18-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	13:05	0.20	26.6	26.6	7.16	7.2	87.3	88.2	3.8	3.8	8	8.0	<2	<2
			26.6		7.3		89.0		3.9		8		<2	
WM4-CB	13:15	0.30	28.6	28.6	7.96	8.0	88.6	88.6	14.5	13.7	7.7	7.7	8	7.5
			28.6		7.97		88.6		12.8		7.7		7	
WM4	13:00	0.20	27.8	27.8	7.53	7.5	81.0	80.6	20.4	20.0	7.8	7.8	19	19.0
			27.8		7.47		80.1		19.6		7.8		19	

Date	20-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	13:05	0.20	26.6	26.6	7.26	7.3	86.1	86.6	3.3	3.0	7.7	7.7	2	2.5
			26.6		7.33		87.0		2.8		7.7		3	
WM4-CB	13:15	0.25	27.9	27.9	7.74	7.8	89.9	89.9	14.1	14.0	7.6	7.6	14	14.0
			27.9		7.76		89.8		13.9		7.6		14	
WM4	13:00	0.23	28.2	28.2	7.29	7.3	89.4	89.2	23.7	23.9	7.7	7.7	24	24.0
			28.2		7.22		89.0		24.1		7.7		24	

Date	22-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	12:15	0.15	27	27.0	8.02	8.0	85.4	84.9	8.6	7.9	8.2	8.2	2	2.0
			27		7.94		84.4		7.3		8.2		2	
WM4-CB	12:25	0.25	28.7	28.7	8.53	8.5	83.4	83.6	10.2	10.5	8	8.0	6	6.0
			28.7		8.55		83.8		10.7		8		6	
WM4	12:10	0.20	27.5	27.5	8.81	8.8	84.1	84.6	23.5	23.3	8.2	8.2	17	15.5
			27.5		8.81		85.1		23.1		8.2		14	

Date	24-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	12:40	0.50	25.2	25.2	8.47	8.5	102.7	102.8	185.0	187.0	7.8	7.8	136	141.0

			25.2		8.49		102.9		189.0		7.8		146	
WM4-CB	12:50	0.50	25.9	25.9	7.87	7.8	96.6	96.0	133.0	134.0	7.6	7.6	102	101.0
			25.9		7.75		95.3		135.0		7.6		100	
WM4	12:30	0.60	25.6	25.6	8.02	8.0	98.2	98.5	213.0	215.0	7.6	7.6	156	158.0
			25.6		8.06		98.7		217.0		7.6		160	

Date	27-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	11:55	0.20	26.8	26.8	7.81	7.8	97.5	96.8	3.1	3.0	7.75	7.8	<2	<2
			26.8		7.69		96.0		2.9		7.75		<2	
WM4-CB	12:05	0.25	28	28.0	6.6	6.7	84.5	85.2	6.9	6.8	7.35	7.4	6	6.0
			28		6.7		85.8		6.7		7.35		6	
WM4	11:50	0.20	27.4	27.4	7.09	7.1	89.8	90.0	12.8	12.7	7.95	8.0	10	9.5
			27.4		7.12		90.1		12.5		7.95		9	

Date	29-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM4-CA	11:35	0.15	26.1	26.1	7.17	7.3	89.1	90.2	7.6	7.8	7.79	7.8	9	8.5
			26.1		7.37		91.2		8.1		7.79		8	
WM4-CB	11:45	0.25	27.5	27.5	6.58	6.6	83.7	84.0	22.3	22.1	7.42	7.4	22	23.0
			27.5		6.65		84.3		21.9		7.42		24	
WM4	11:30	0.20	26.3	26.3	7.06	7.1	87.7	87.9	13.3	13.7	7.82	7.8	11	10.5
			26.3		7.08		88.0		14.1		7.82		10	

Water Quality Monitoring Data for Contract 6

Date: 1-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:30	0.35	25	25.0	8.08	8.1	97.8	97.9	353.0	364.5	6.90	6.9	336	334.5
			25		8.1		98.0		376.0		6.90		333	
WM2A	10:20	0.25	25.3	25.3	7.86	7.9	95.4	95.5	367.0	358.0	6.90	6.9	266	267.0
			25.3		7.86		95.5		349.0		6.90		268	

Date: 3-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:30	0.25	25.2	25.2	7.9	7.9	95.3	95.5	21.3	21.8	6.90	6.9	6	6.0
			25.2		7.92		95.7		22.2		6.90		6	
WM2A	10:20	0.20	25.8	25.8	7.29	7.3	89.1	89.4	62.7	62.9	7.00	7.0	66	65.0
			25.8		7.31		89.7		63.1		7.00		64	

Date: 4-Sep-18#														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	9:40	0.25							5.2	5.2			7	7.0
							5.2		7					
WM2A	9:30	0.20							11.7	11.9			10	10.0
							12.1		10					

Date: 5-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:30	0.25	29.4	29.4	5.73	5.7	74.4	73.5	11.4	11.4	7.90	7.9	4	4.0
			29.4		5.59		72.5		11.3		7.90		4	
WM2A	10:15	0.20	29	29.0	5.42	5.4	70.6	70.7	22.9	22.2	8.20	8.2	16	16.0
			29		5.44		70.7		21.5		8.20		16	

Date: 7-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:50	0.25	27.2	27.2	7.01	7.0	84.0	83.8	7.3	7.3	8.40	8.4	<2	<2
			27.2		6.95		83.6		7.3		8.40		<2	
WM2A	10:40	0.20	27.1	27.1	6.82	6.8	82.7	82.3	23.9	24.1	7.50	7.5	19	19.0
			27.1		6.76		81.9		24.2		7.50		19	

Date: 11-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	11:00	0.25	25.3	25.3	6.61	6.6	73.3	73.5	10.8	11.2	8.70	8.7	2	2.0
			25.3		6.65		73.7		11.6		8.70		2	
WM2A	10:40	0.23	25.7	25.7	7.03	7.0	81.7	81.9	21.8	21.8	8.70	8.7	14	14.0
			25.7		7.05		82.1		21.7		8.70		14	

Date: 13-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:45	0.23	25	25.0	6.55	6.5	72.2	72.0	11.1	11.0	8.90	8.9	4	4.0
			25		6.48		71.7		10.9		8.90		4	

Agreement No. CE 45/2008 (CE)
 Liantang/Heung Yuen Wai Boundary Control Point and Associated Works
 Monthly Environmental Monitoring & Audit Report (No.62) – September 2018



WM2A	10:35	0.20	25.5 25.5	25.5	7 7.1	7.1	77.0 78.0	77.5	9.5 8.9	9.2	8.10 8.10	8.1	4 4	4.0
------	-------	------	--------------	------	----------	-----	--------------	------	------------	-----	--------------	-----	--------	-----

Date	15-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:50	0.20	25.6	25.6	6.98	7.0	77.1	77.5	10.8	10.5	8.00	8.0	2	2.0
			25.6		7.02		77.8		10.2		8.00		<2	
WM2A	10:30	0.20	27.3	27.3	6.7	6.7	76.7	76.9	12.9	12.6	7.80	7.8	8	8.0
			27.3		6.71		77.0		12.3		7.80		8	

Date	18-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:20	0.25	25.1	25.1	6.88	6.7	77.8	77.9	9.4	9.9	8.10	8.1	<2	<2
			25.1		6.6		78.0		10.3		8.10		<2	
WM2A	10:05	0.20	26	26.0	7.03	7.1	81.1	81.6	32.9	33.5	7.90	7.9	27	27.5
			26		7.07		82.0		34.1		7.90		28	

Date	20-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	11:25	0.23	26.1	26.1	6.4	6.4	72.0	71.7	4.9	4.9	7.70	7.7	2	3.0
			26.1		6.31		71.4		4.9		7.70		4	
WM2A	10:55	0.20	26.6	26.6	6.33	6.2	71.8	71.0	12.2	12.6	7.70	7.7	10	10.5
			26.6		6.1		70.1		12.9		7.70		11	

Date	21-Sep-18#													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	11:40	0.25							4.1	3.9			<2	<2
									3.8		<2			
WM2A	11:30	0.20							7.1	7.0			4	4.0
									7.0		4			

Date	22-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	11:10	0.24	25.4	25.4	6.76	6.8	73.8	73.9	6.4	6.2	8.00	8.0	<2	<2
			25.4		6.78		74.0		6.0		8.00		<2	
WM2A	10:55	0.20	26.2	26.2	6.41	6.4	71.1	71.1	17.1	17.8	8.00	8.0	14	14.5
			26.2		6.37		71.0		18.5		8.00		15	

Date	24-Sep-18													
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	11:25	0.25	25.5	25.5	6.63	6.7	77.1	77.6	10.2	10.2	7.80	7.8	6	9.0
			25.5		6.7		78.0		10.2		7.80		12	
WM2A	11:05	0.20	25.9	25.9	6.81	6.8	79.0	78.5	123.0	128.5	7.90	7.9	134	131.5
			25.9		6.79		77.9		134.0		7.90		129	

Agreement No. CE 45/2008 (CE)
 Liantang/Heung Yuen Wai Boundary Control Point and Associated Works
 Monthly Environmental Monitoring & Audit Report (No.62) – September 2018



Date														
26-Sep-18#														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	13:40	0.25							5.8	5.8			7	7.0
								5.8	7					
WM2A	13:30	0.20							15.9	15.6			14	14.0
								15.3	14					

Date														
27-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:55	0.20	25.4	25.4	7.65	7.7	93.5	93.9	6.1	6.1	7.13	7.1	3	2.5
			25.4		7.73		94.3		6.2		7.13		2	
WM2A	10:35	0.20	25.9	25.9	6.82	6.9	84.0	84.4	81.7	82.9	7.09	7.1	88	88.0
			25.9		6.88		84.7		84.1		7.09		88	

Date														
28-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:25	0.25							5.3	5.6			4	4.0
								5.9	4					
WM2A	10:15	0.20							17.8	17.8			12	12.0
								17.8	12					

Date														
29-Sep-18														
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM2A-C	10:30	0.23	23.7	23.7	7.44	7.5	88.0	88.1	5.0	5.0	7.44	7.4	<2	<2
			23.7		7.46		88.2		5.0		7.44		<2	
WM2A	10:20	0.20	24.6	24.6	6.73	6.8	80.9	81.4	15.4	15.4	7.62	7.6	14	14.0
			24.6		6.8		81.8		15.4		7.62		14	

Remarks: # Additional water quality monitoring for the parameters with Action/Limit Level exceedance triggered only.

	Action Level
	Limit Level

Water Quality Monitoring Data for Contract 2 and 6

Date		1-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	10:55	0.20	25.2	25.2	7.31	7.3	90.8	90.1	Overage	over range	6.9	6.9	670	672.0
			25.2		7.33		89.3		Overage		6.9		674	
WM3	11:05	0.35	25.2	25.2	7.23	7.2	87.6	87.8	351.0	351.5	6.9	6.9	248	245.5
			25.2		7.24		88.0		352.0		6.9		243	

Date		3-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	10:55	0.20	27.5	27.5	7.4	7.3	90.1	90.4	101.0	99.3	8.3	8.3	98	98.5
			27.5		7.16		90.7		97.6		8.3		99	
WM3	11:10	0.20	26.6	26.6	6.58	6.6	81.6	82.1	20.4	20.3	7.4	7.4	17	17.0
			26.6		6.63		82.5		20.1		7.4		17	

Date		5-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	10:55	0.18	30.2	30.2	5.99	6.0	79.5	79.2	13.3	12.6	10.3	10.3	23	22.5
			30.2		5.94		78.8		11.9		10.3		22	
WM3	11:10	0.18	32.1	32.1	6.24	6.2	85.6	85.3	13.3	13.3	9.6	9.6	17	17.0
			32.1		6.2		84.9		13.2		9.6		17	

Date		7-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:10	0.15	30.6	30.6	6.94	6.9	76.2	75.7	11.5	11.5	10.2	10.2	22	21.5
			30.6		6.87		75.2		11.4		10.2		21	
WM3	11:25	0.16	30	30.0	6.22	6.2	72.1	72.2	5.9	6.0	8.2	8.2	<2	<2
			30		6.21		72.2		6.2		8.2		<2	

Date		11-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:15	0.16	26.9	26.9	7.63	7.6	86.1	85.9	22.4	21.6	10.7	10.7	38	38.5
			26.9		7.6		85.6		20.8		10.7		39	
WM3	11:25	0.18	26.9	26.9	6.95	7.0	77.3	77.6	4.4	4.4	9.8	9.8	3	3.0
			26.9		6.97		77.8		4.3		9.8		3	

Date		13-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:05	0.15	26.9	26.9	7.34	7.4	84.5	84.4	3.4	3.5	11.2	11.2	7	6.5
			26.9		7.36		84.2		3.6		11.2		6	
WM3	11:15	0.15	27.5	27.5	7.75	7.8	88.9	89.1	13.0	13.2	9.3	9.3	10	10.0
			27.5		7.76		89.2		13.3		9.3		10	

Date		15-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:05	0.14	28.8	28.8	7.11	7.2	86.5	86.7	7.2	7.4	10.8	10.8	5	5.5
			28.8		7.2		86.9		7.5		10.8		6	

WM3	11:15	0.15	28 28	28.0	7.8 7.97	7.9	92.1 93.1	92.6	11.0 11.1	11.1	9.2 9.2	9.2	7 7	7.0
-----	-------	------	----------	------	-------------	-----	--------------	------	--------------	------	------------	-----	--------	-----

Date		18-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	10:45	0.18	27.8	27.8	7.81	7.8	90.6	90.2	15.8	16.5	10.8	10.8	63	62.5
			27.8		7.76		89.7		17.1		10.8		62	
WM3	11:00	0.20	29.1	29.1	7.82	7.8	92.9	92.0	18.9	19.0	8.7	8.7	25	24.5
			29.1		7.71		91.1		19.1		8.7		24	

Date		20-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:45	0.16	28	28.0	6.94	6.9	82.8	82.8	3.9	3.6	10.4	10.4	9	9.0
			28		6.93		82.7		3.3		10.4		9	
WM3	12:00	0.20	27.7	27.7	6.71	6.8	82.8	83.3	11.9	11.9	8.7	8.7	12	12.5
			27.7		6.79		83.8		11.8		8.7		13	

Date		22-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:35	0.20	28	28.0	7.32	7.3	82.1	82.2	38.2	38.4	10.3	10.3	102	100.5
			28		7.33		82.3		38.5		10.3		99	
WM3	11:45	0.20	26.9	26.9	7.8	7.8	83.7	83.8	11.0	10.5	8.8	8.8	4	3.5
			26.9		7.83		83.8		10.0		8.8		3	

Date		24-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:50	0.20	26.5	26.5	7.46	7.5	88.0	88.1	145.0	145.0	8.2	8.2	232	243.0
			26.5		7.47		88.2		145.0		8.2		254	
WM3	12:05	0.30	27	27.0	7.95	7.9	93.0	92.4	170.0	171.0	8.2	8.2	250	263.5
			27		7.87		91.7		172.0		8.2		277	




Date		27-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	11:20	0.15	27.7	27.7	6.84	6.9	87.4	87.7	2.7	2.6	11.34	11.3	5	5.5
			27.7		6.88		88.0		2.5		11.34		6	
WM3	11:30	0.15	26.9	26.9	7.72	9.0	96.2	95.4	7.0	7.1	9.19	9.2	5	5.5
			26.9		7.54		94.6		7.3		9.19		6	




Date		29-Sep-18												
Location	Time	Depth (m)	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		SS(mg/L)	
WM3-C	10:45	0.15	26.9	26.9	6.75	6.8	84.7	84.8	2.7	2.7	10.83	10.8	<2	<2
			26.9		6.76		84.9		2.8		10.83		<2	
WM3	11:00	0.18	28.5	28.5	6.45	6.5	83.1	83.2	13.4	13.4	8.83	8.8	9	10.0
			28.5		6.45		83.2		13.3		8.83		11	




Appendix J

Graphical Plots for Monitoring Result




Air Quality – 1-hour TSP

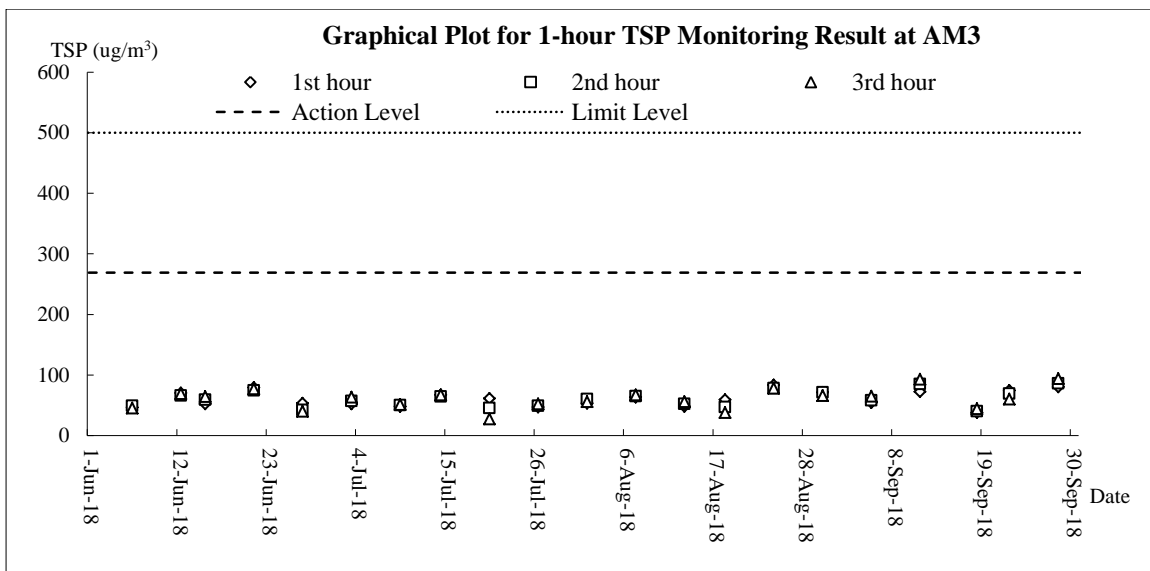
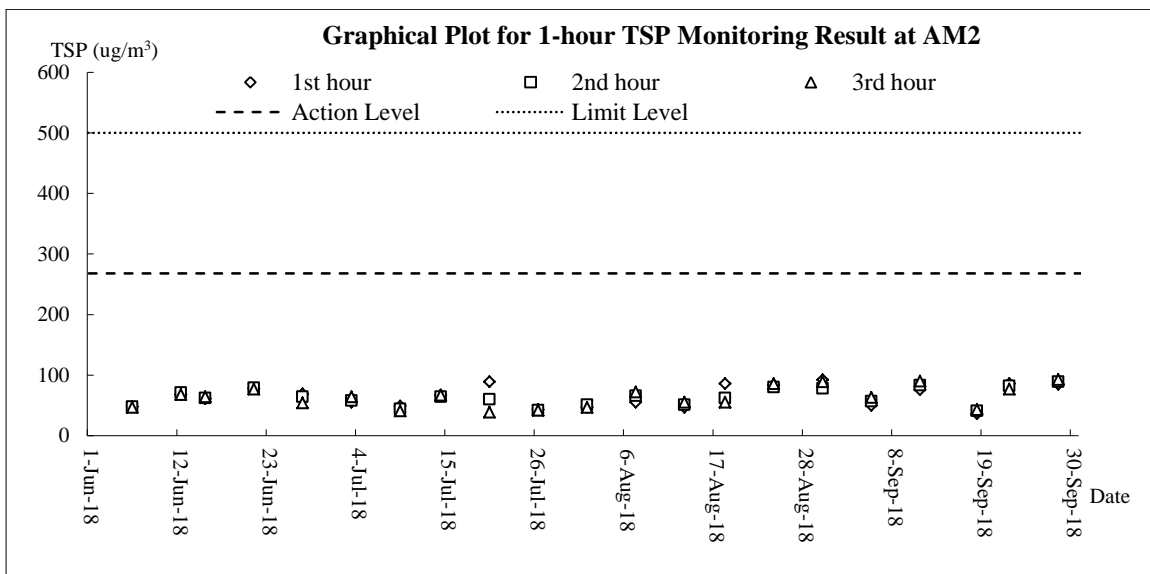
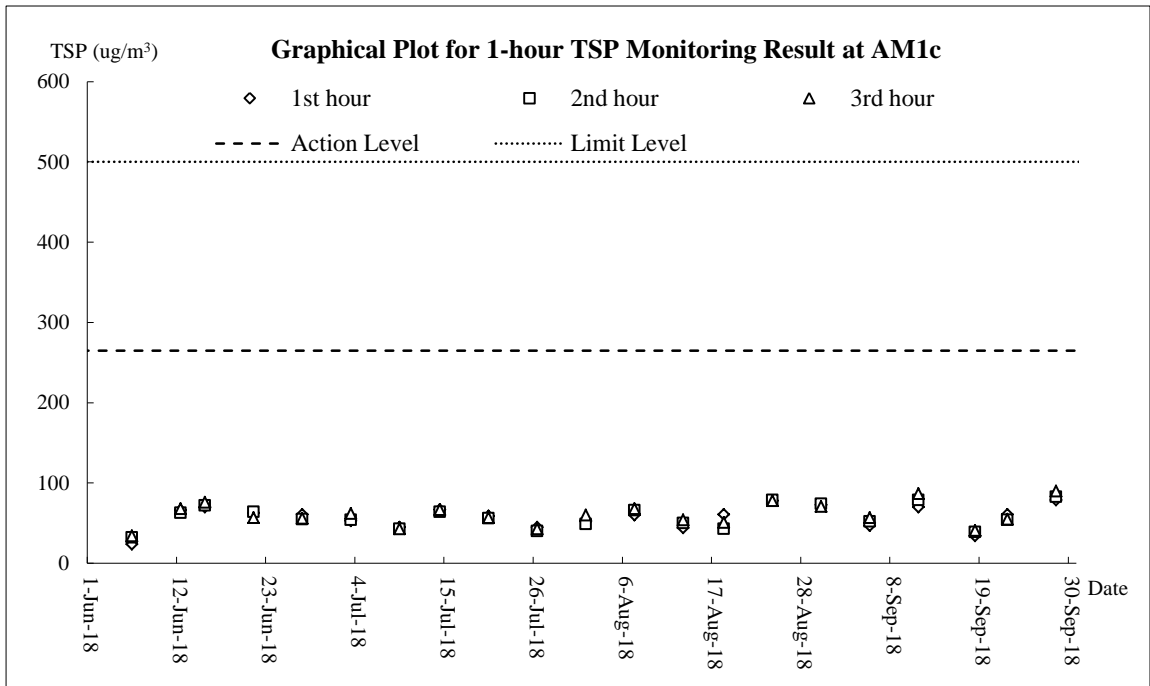


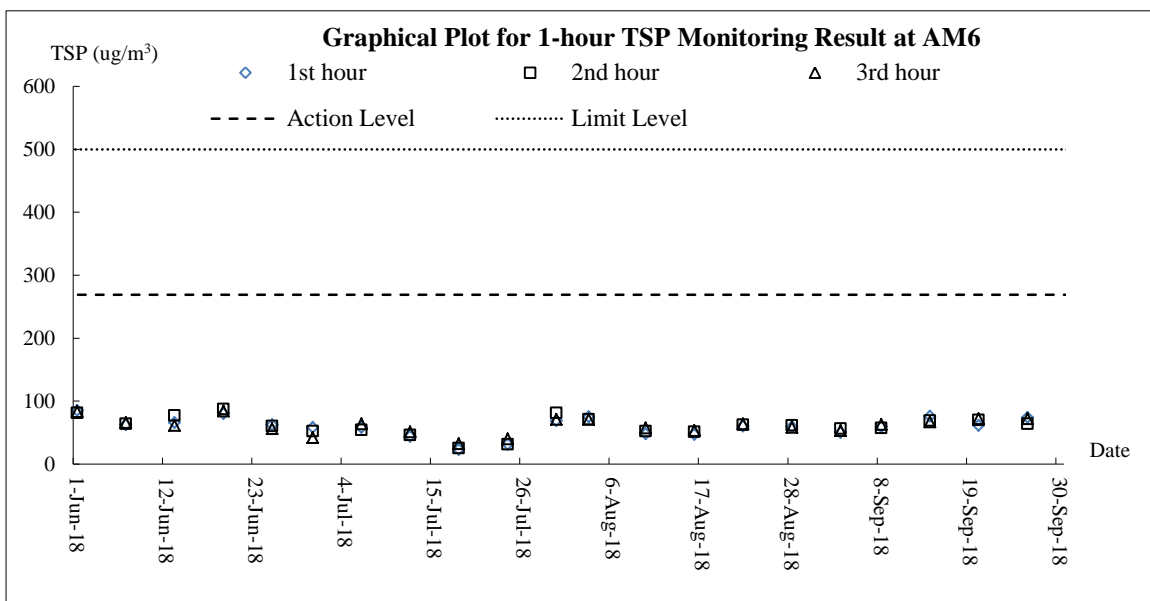
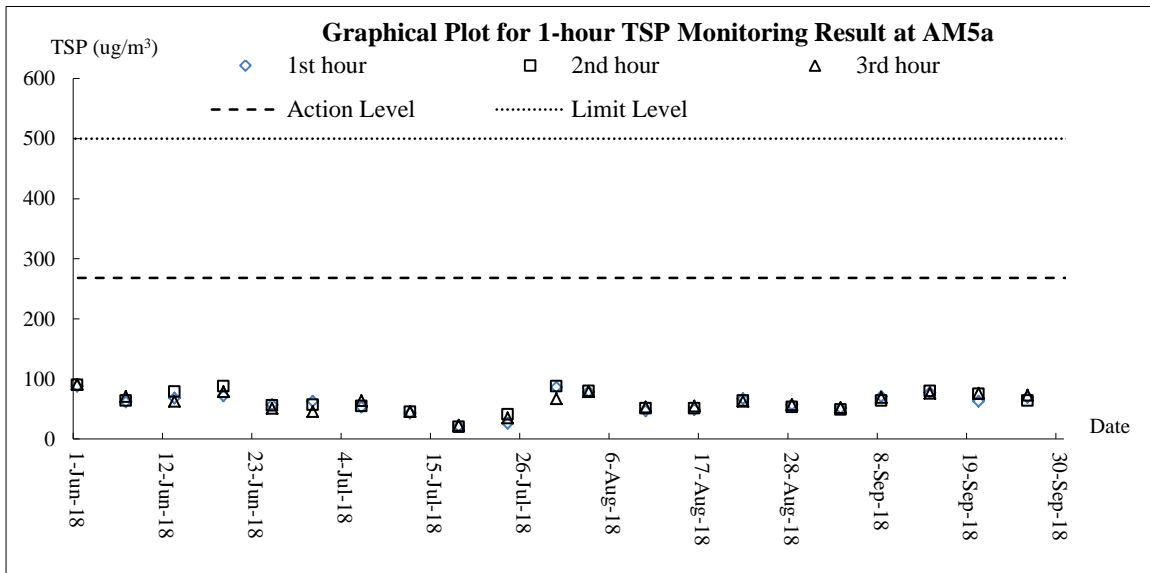
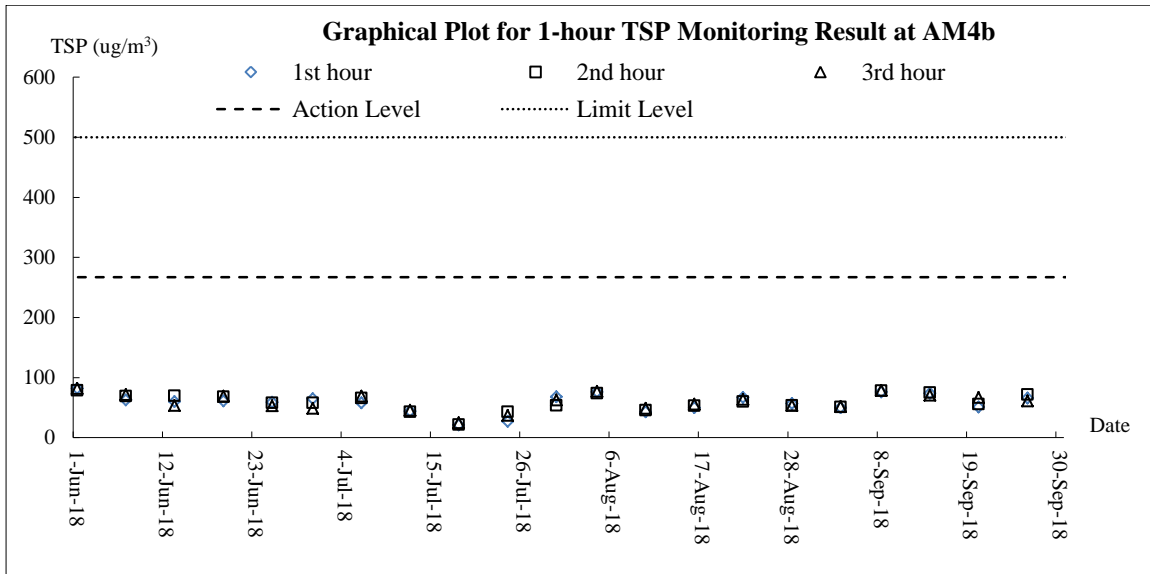


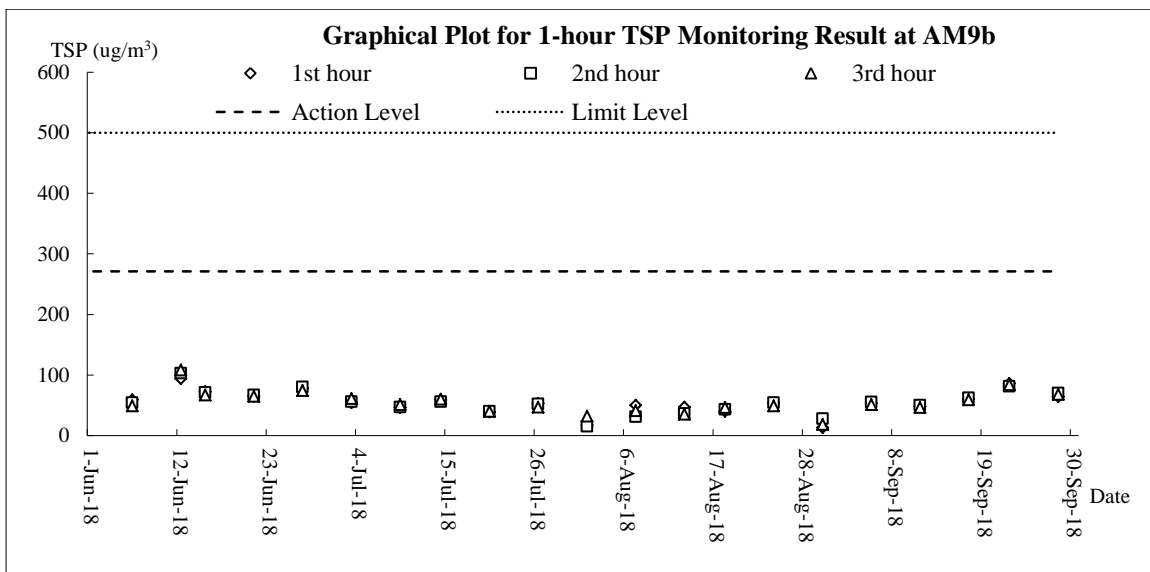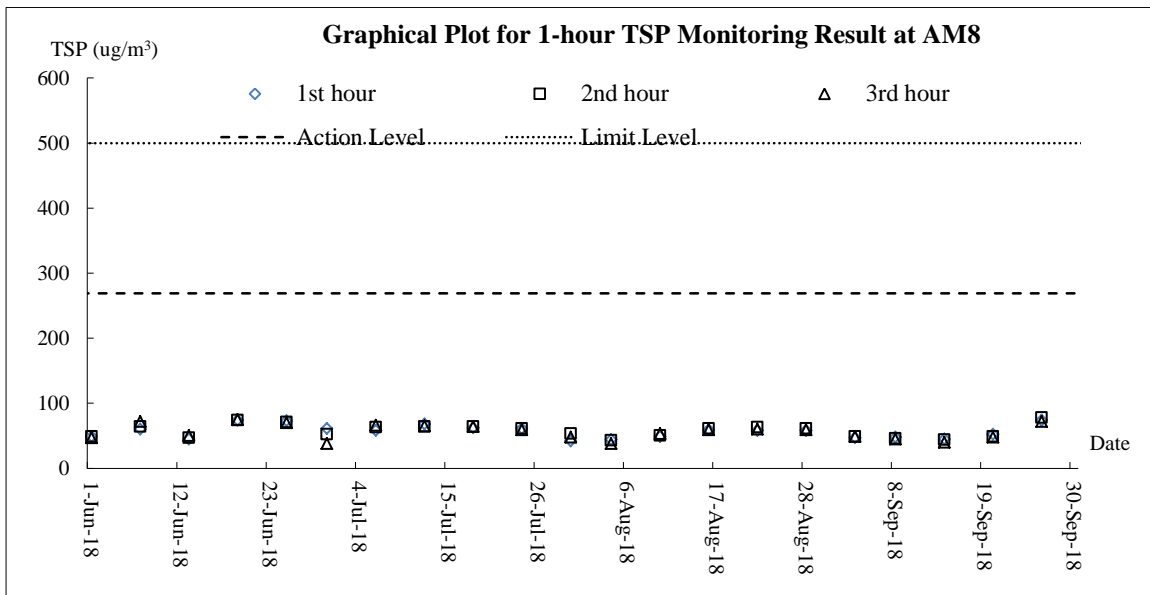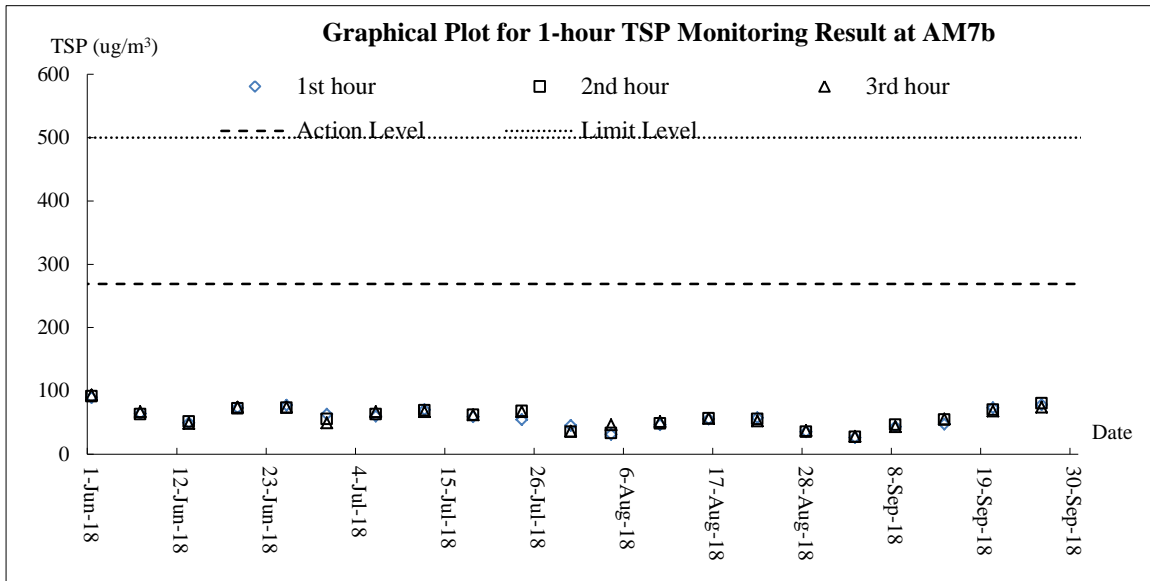




Air Quality – 24-hour TSP

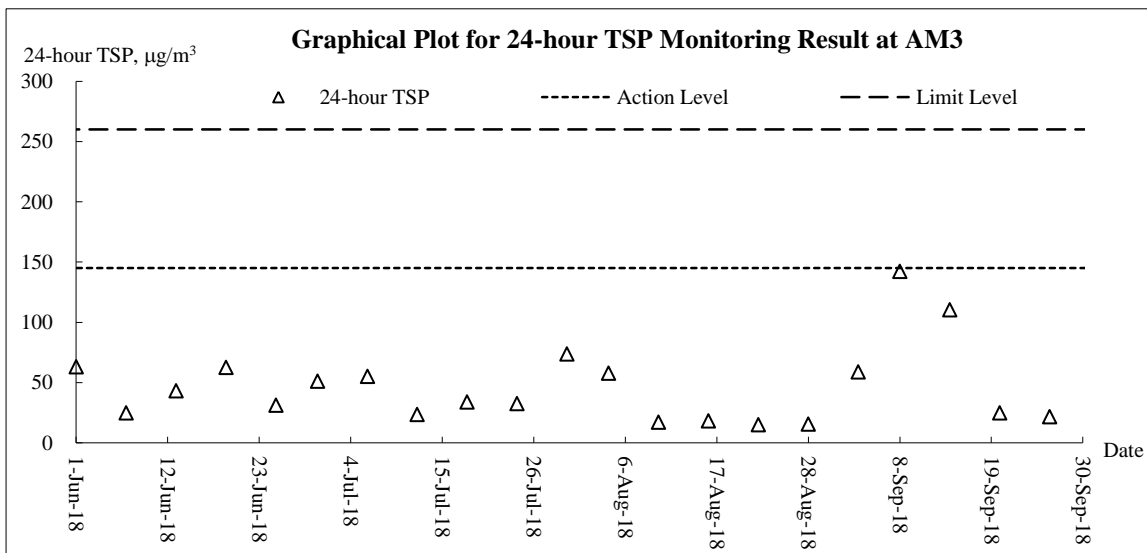
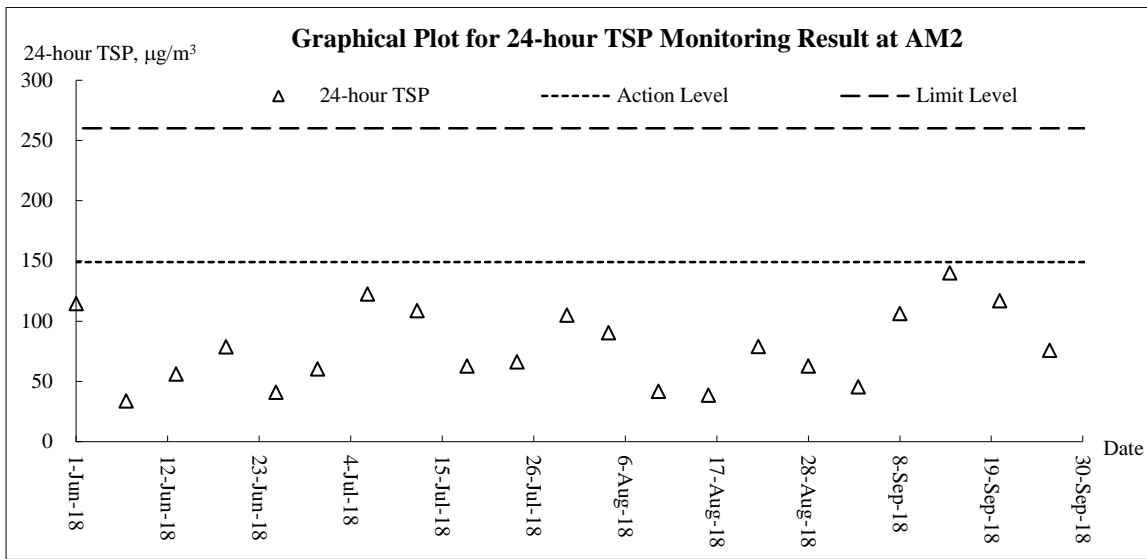
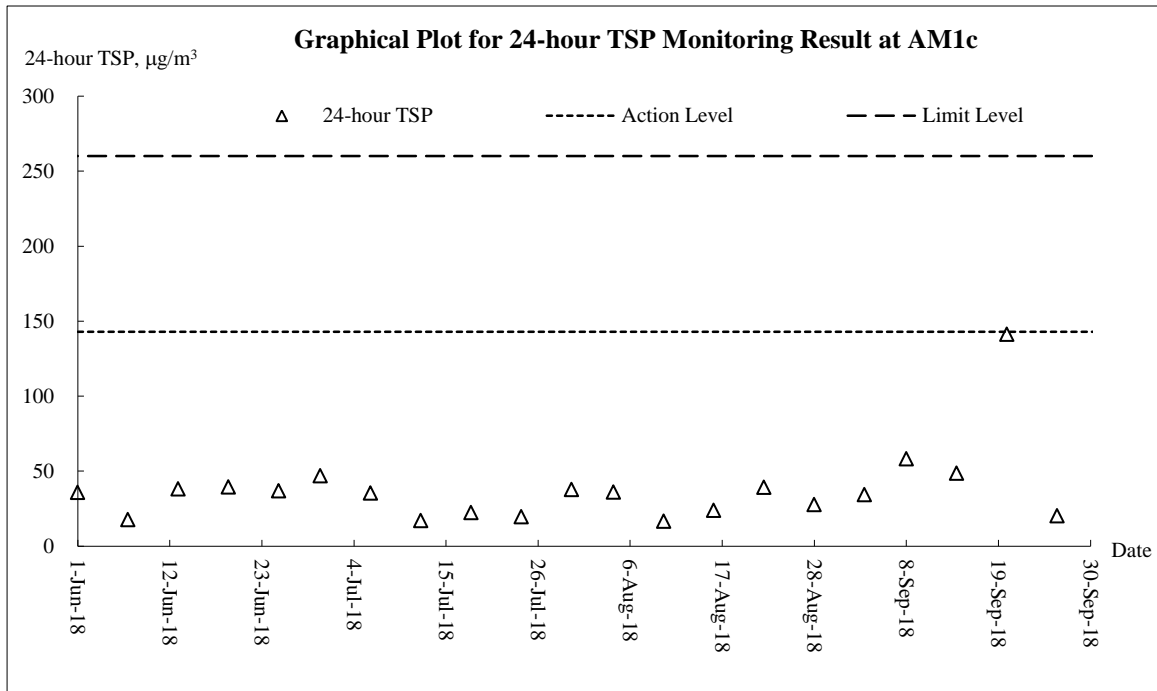


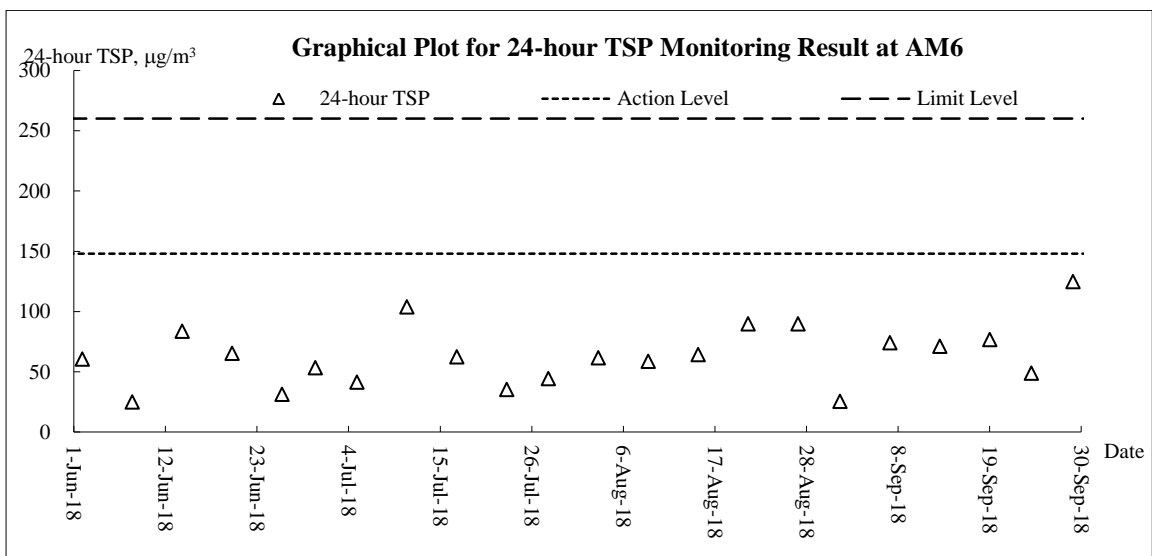
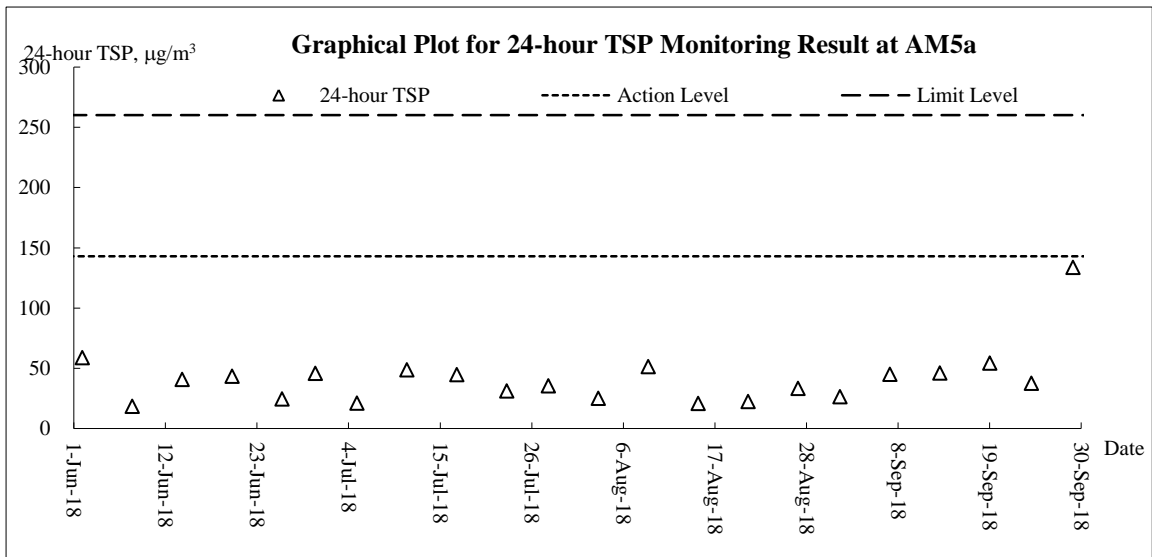
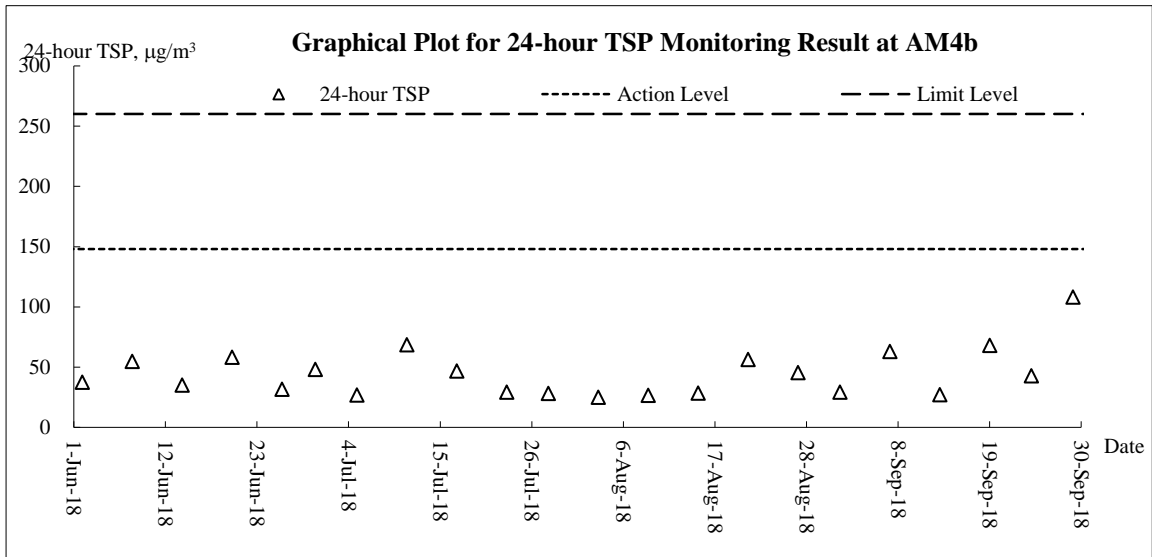


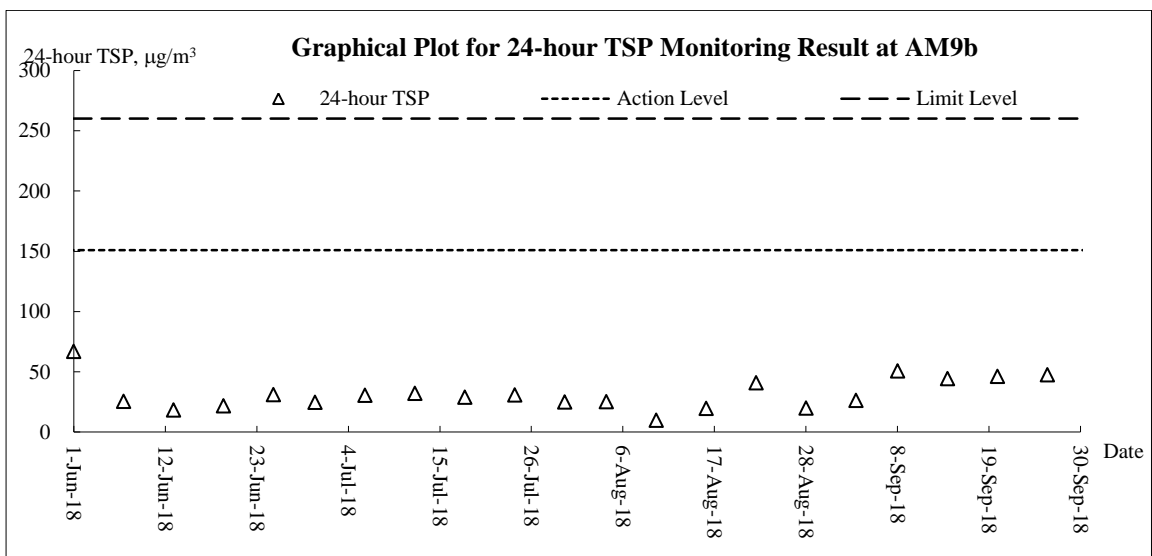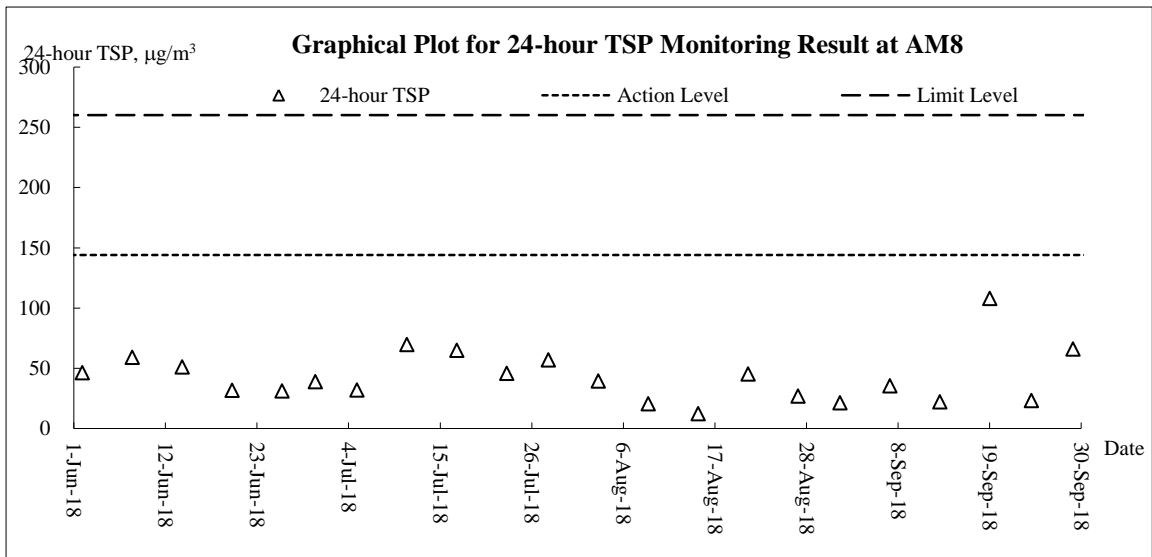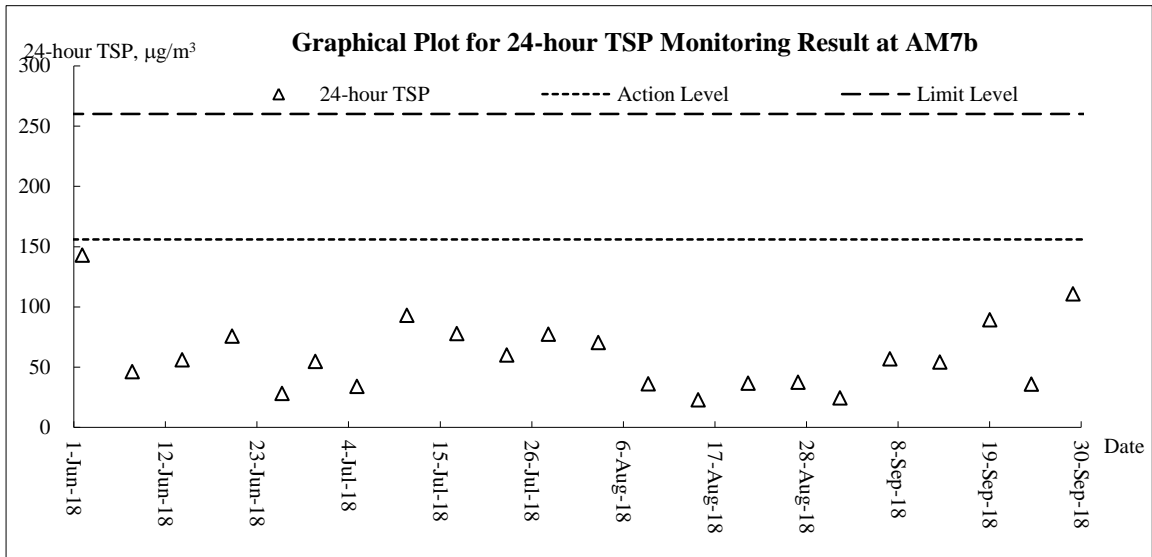


Noise

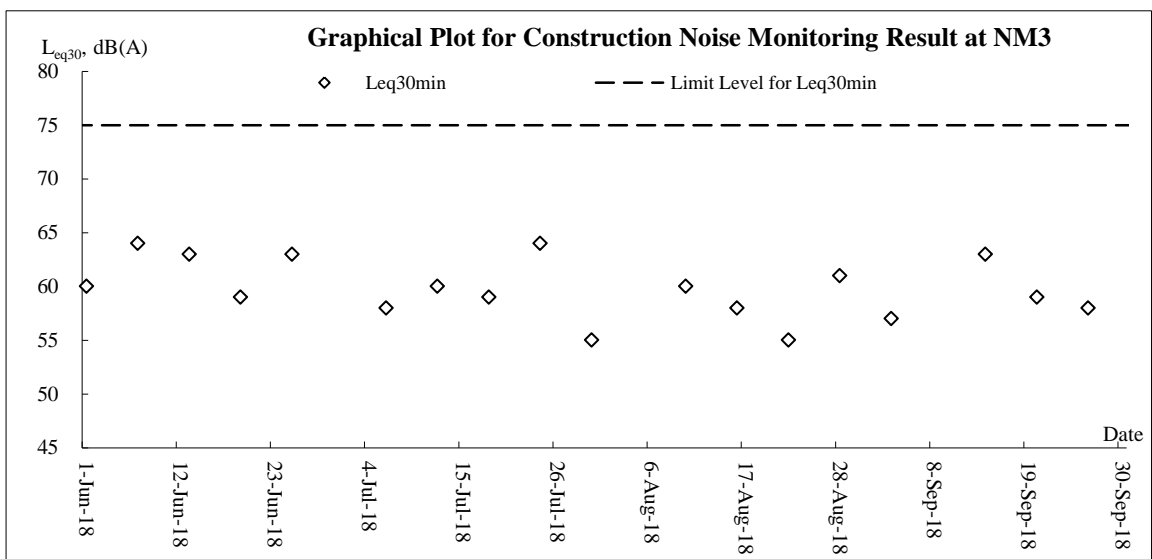
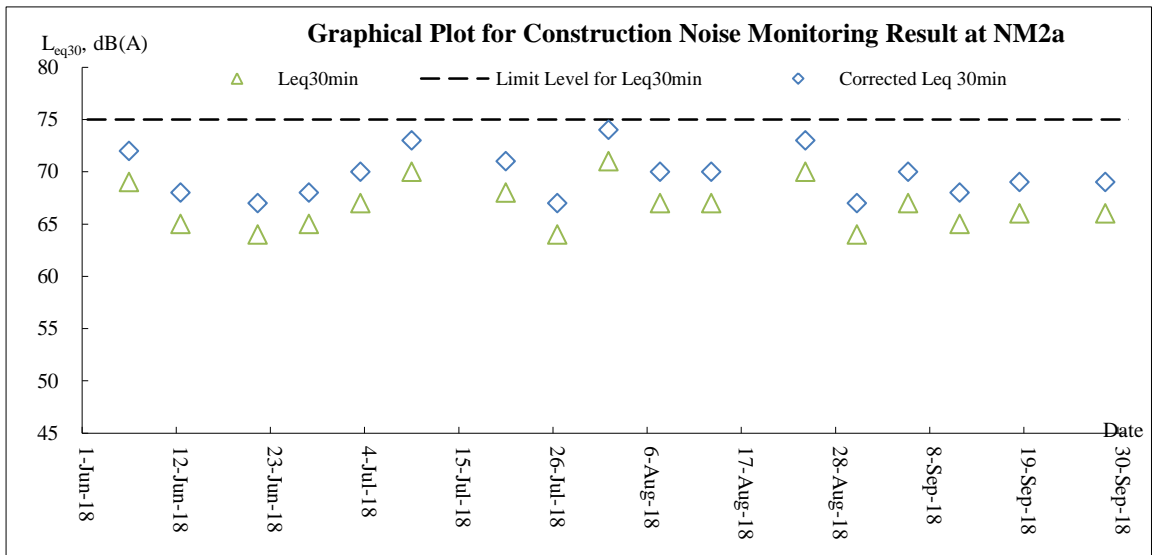
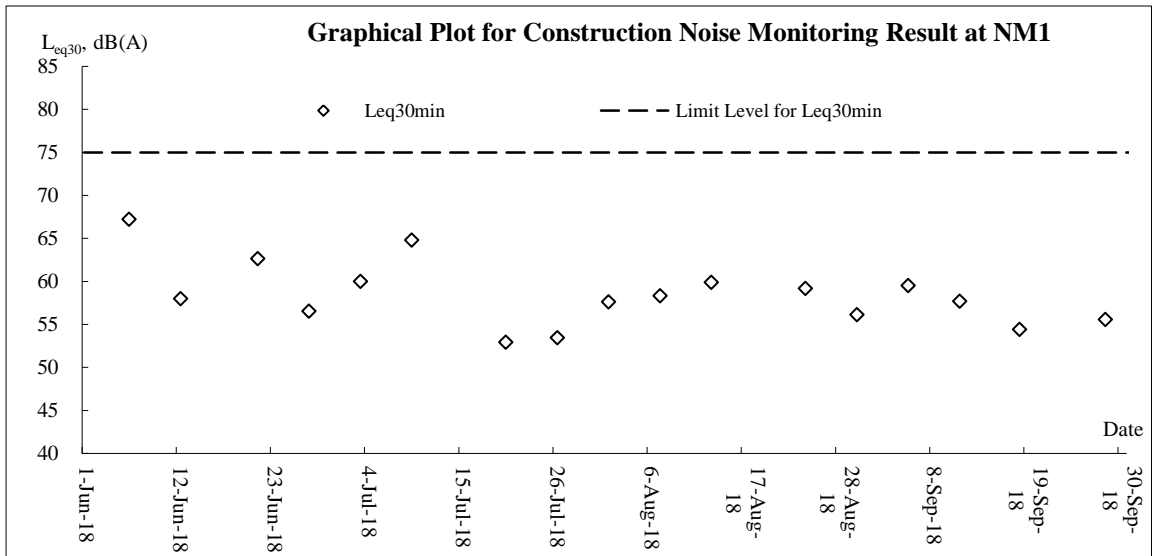


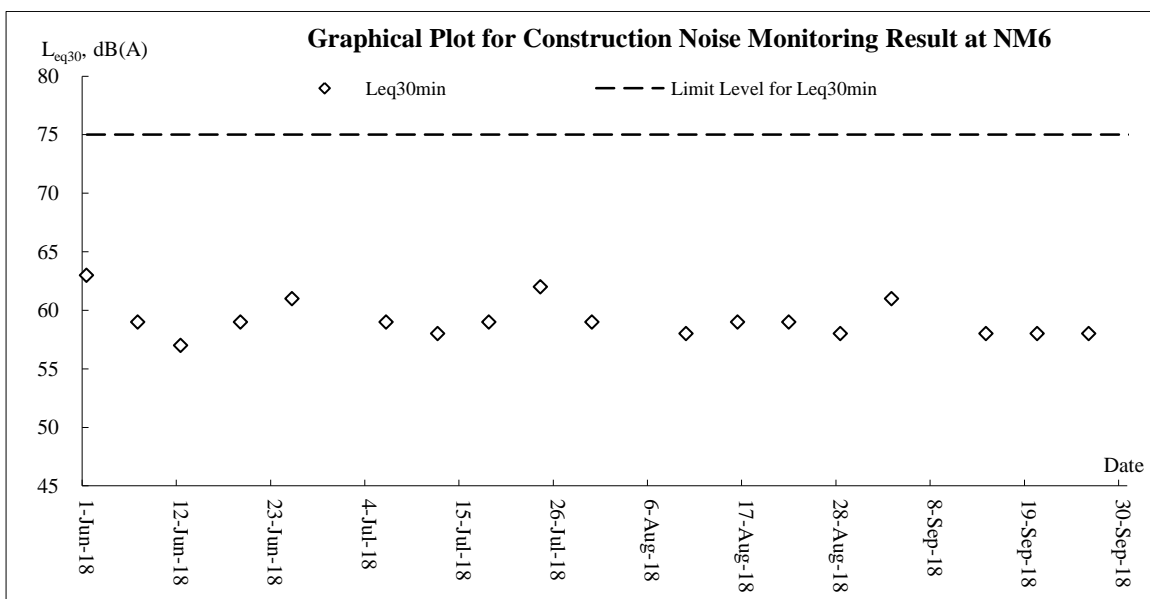
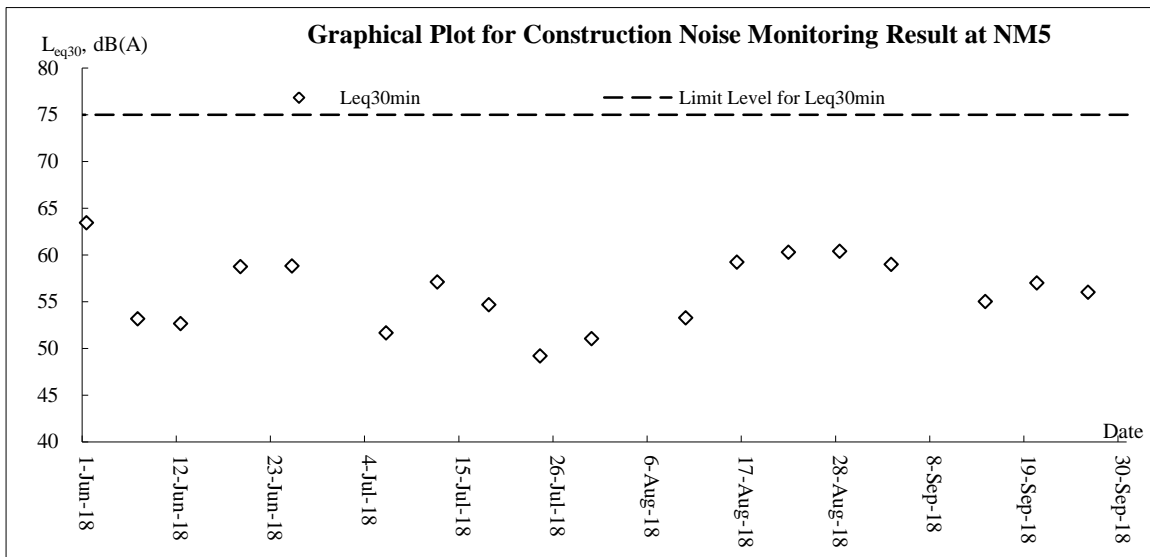
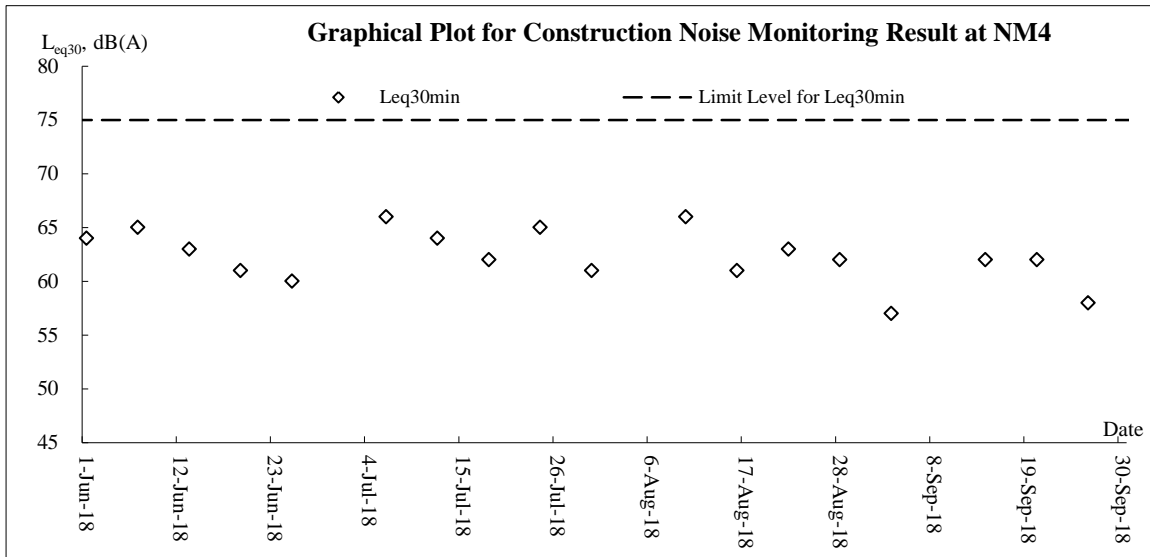


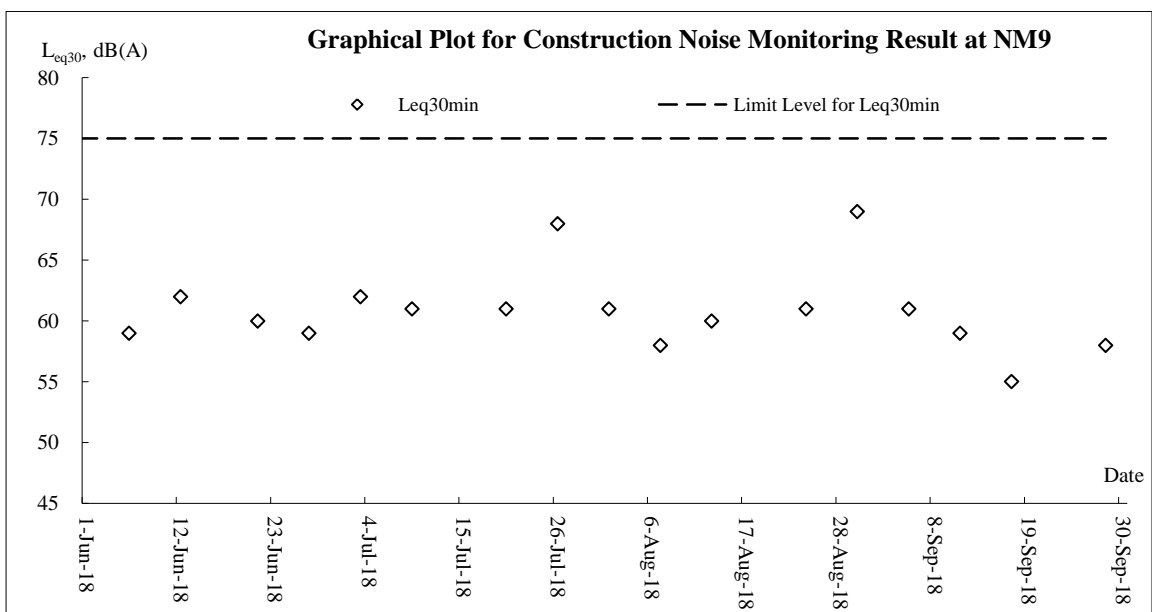
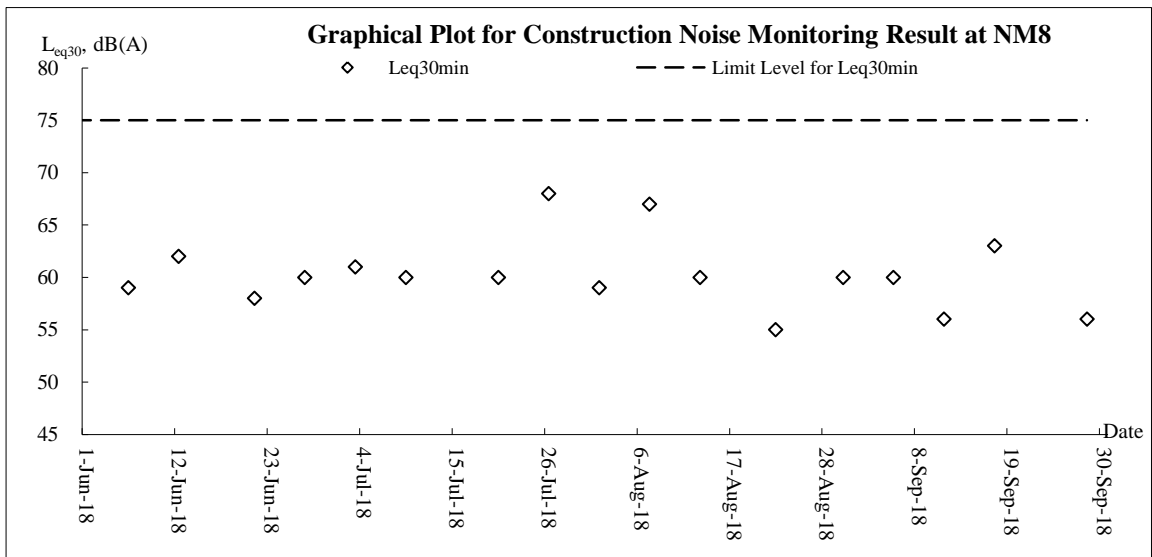
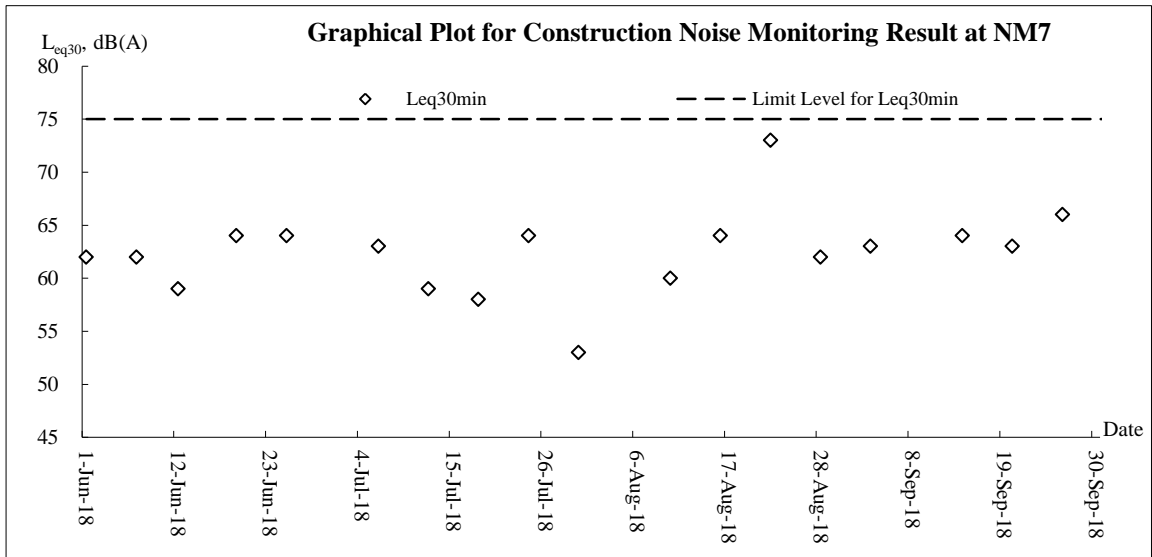




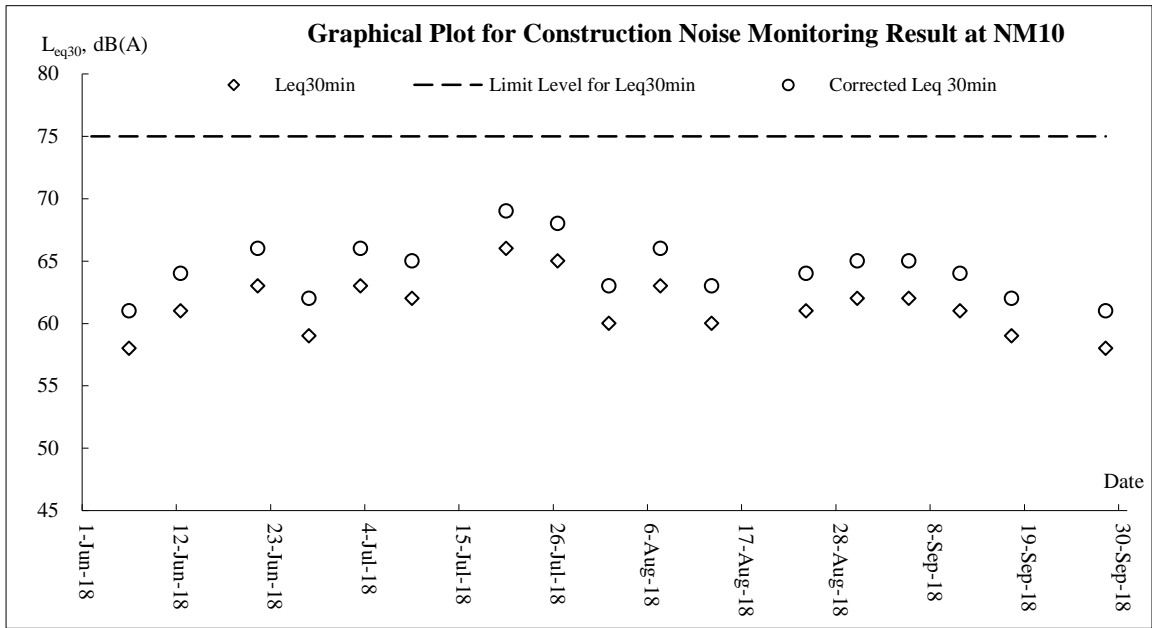


Water Quality

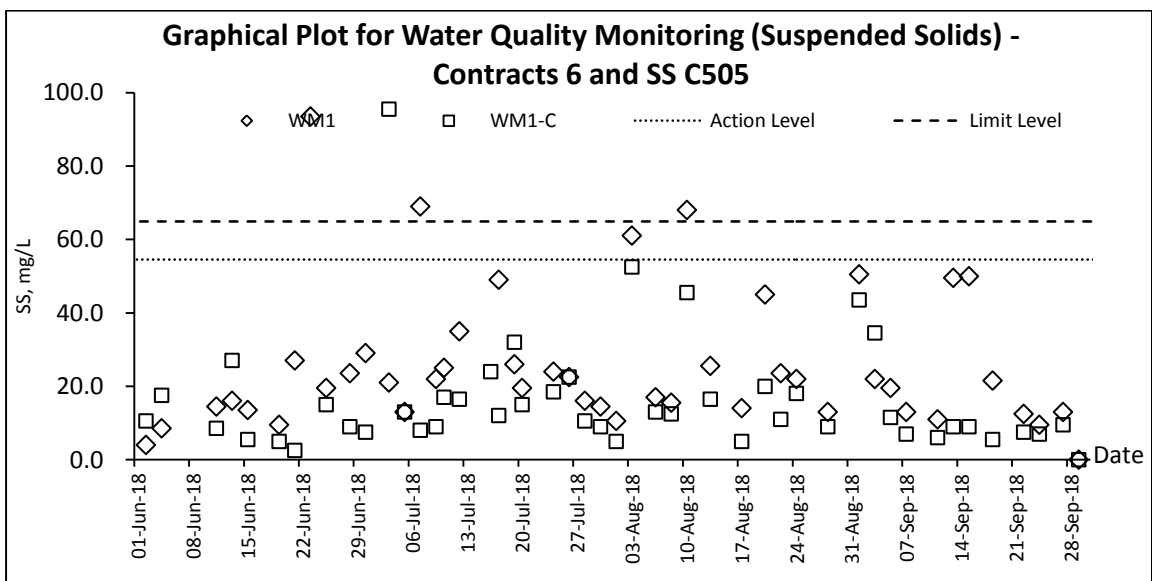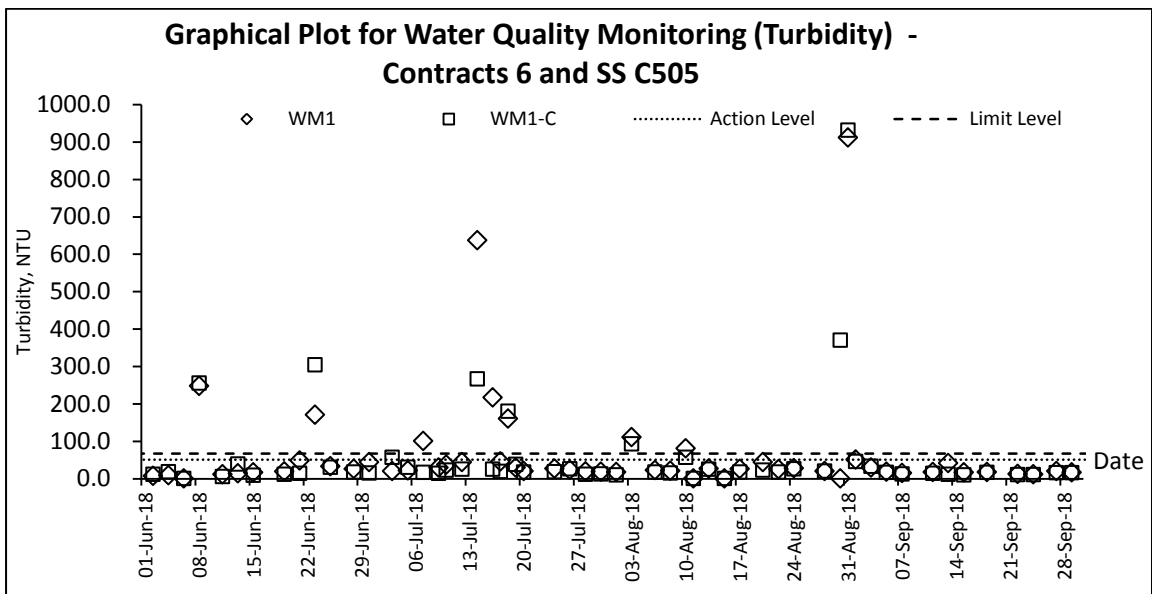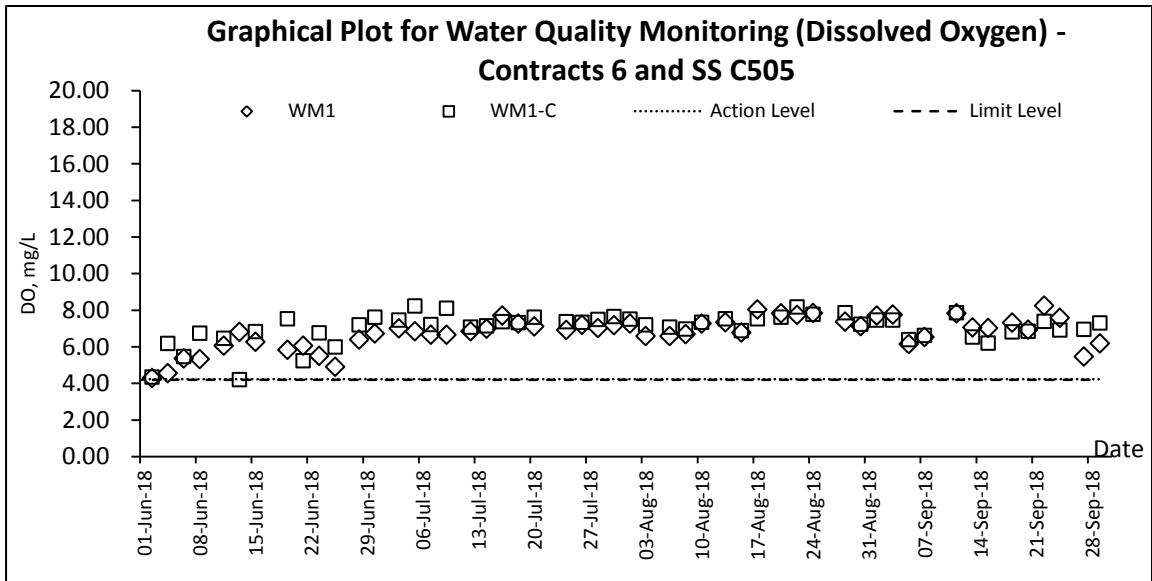

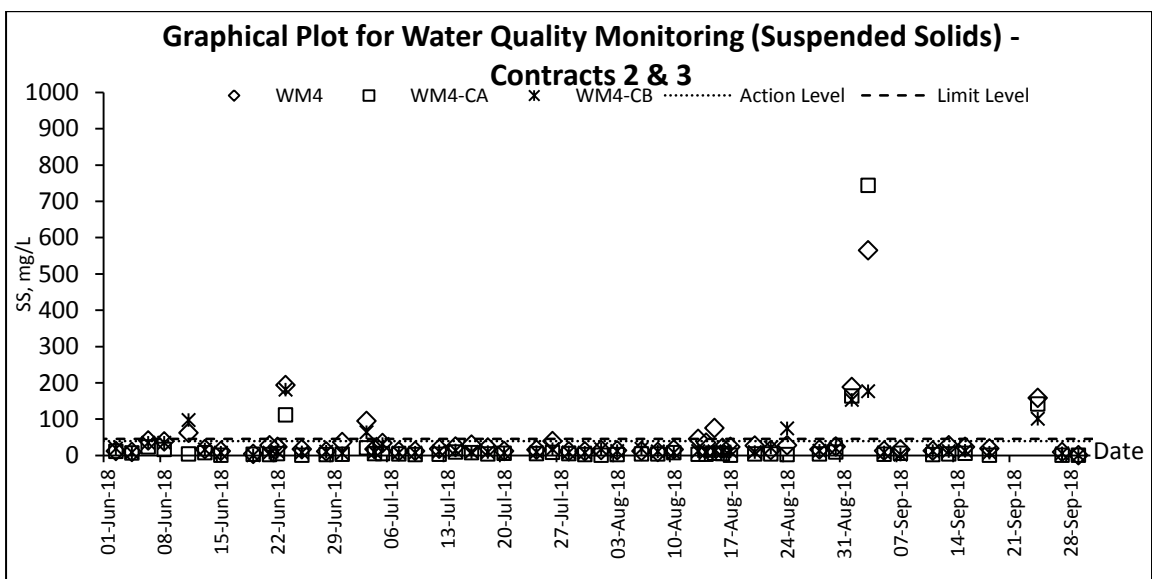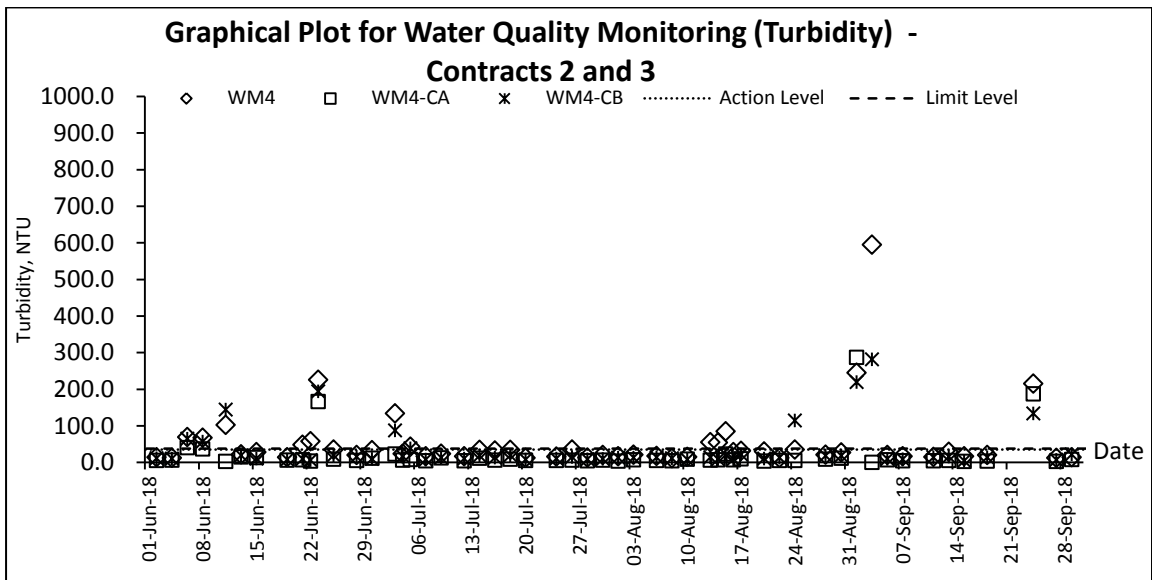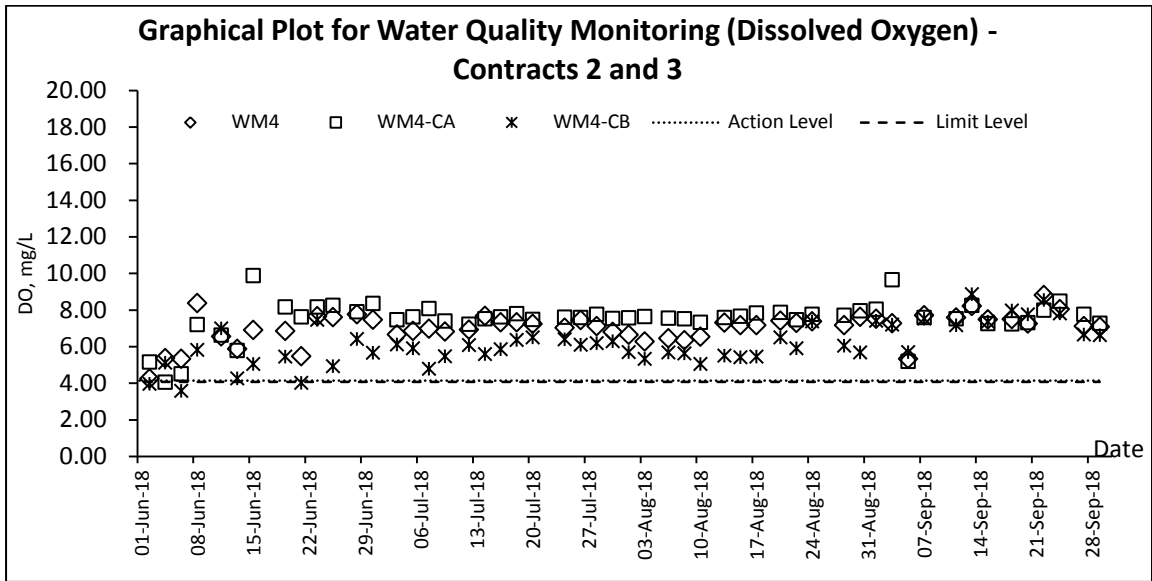

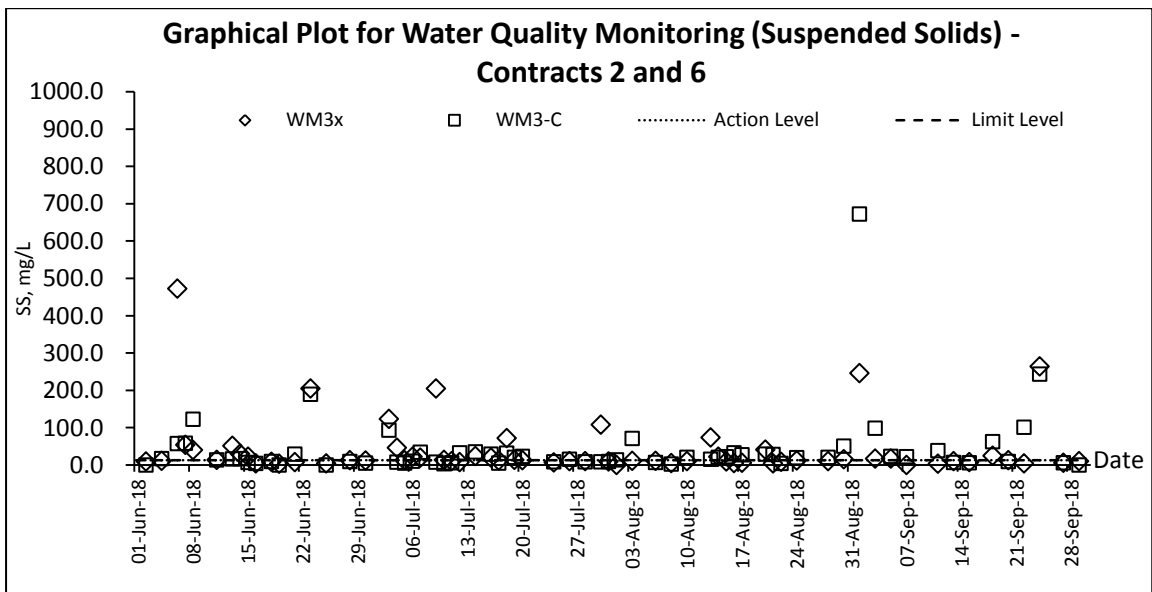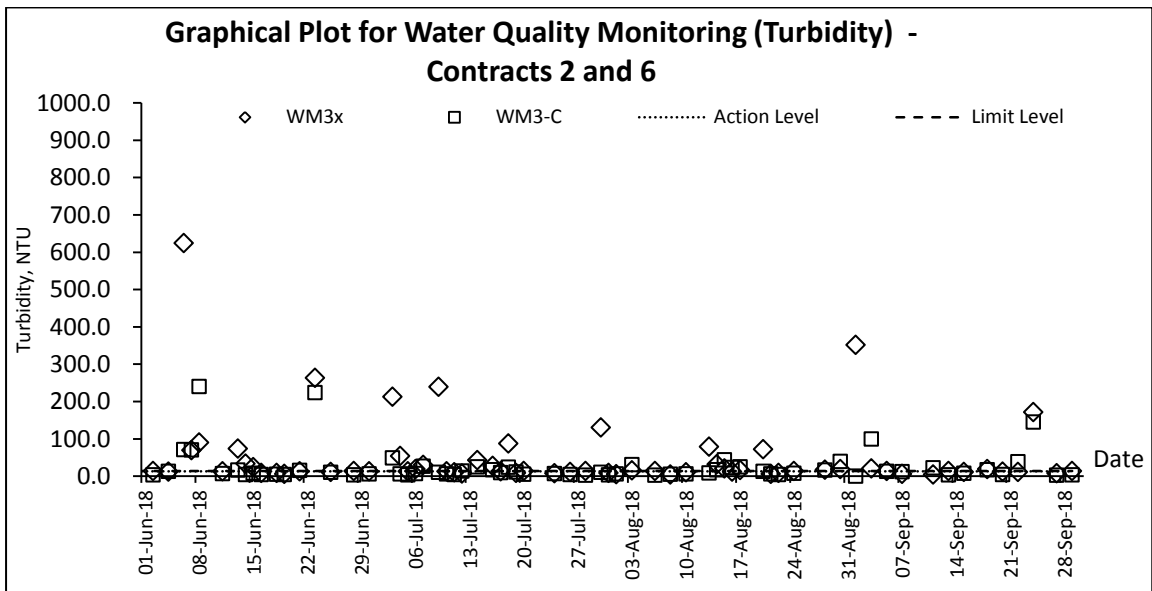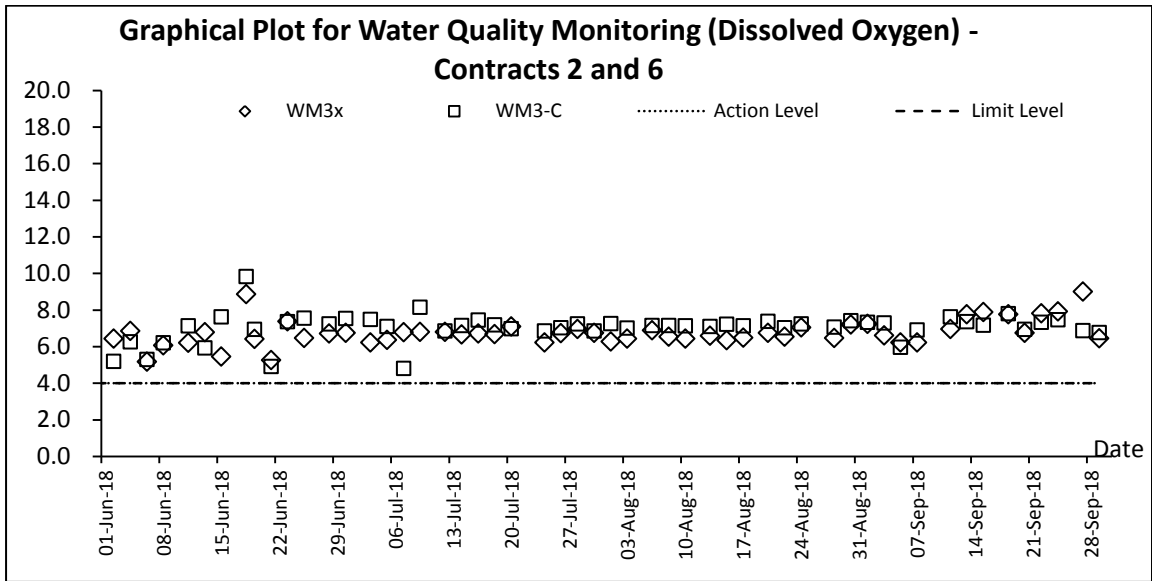

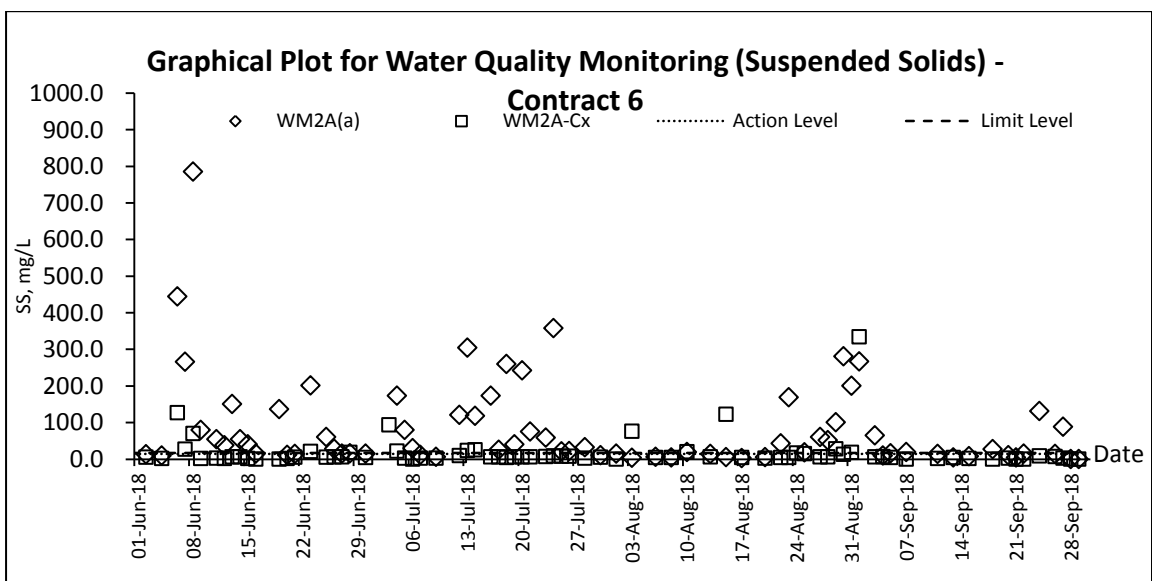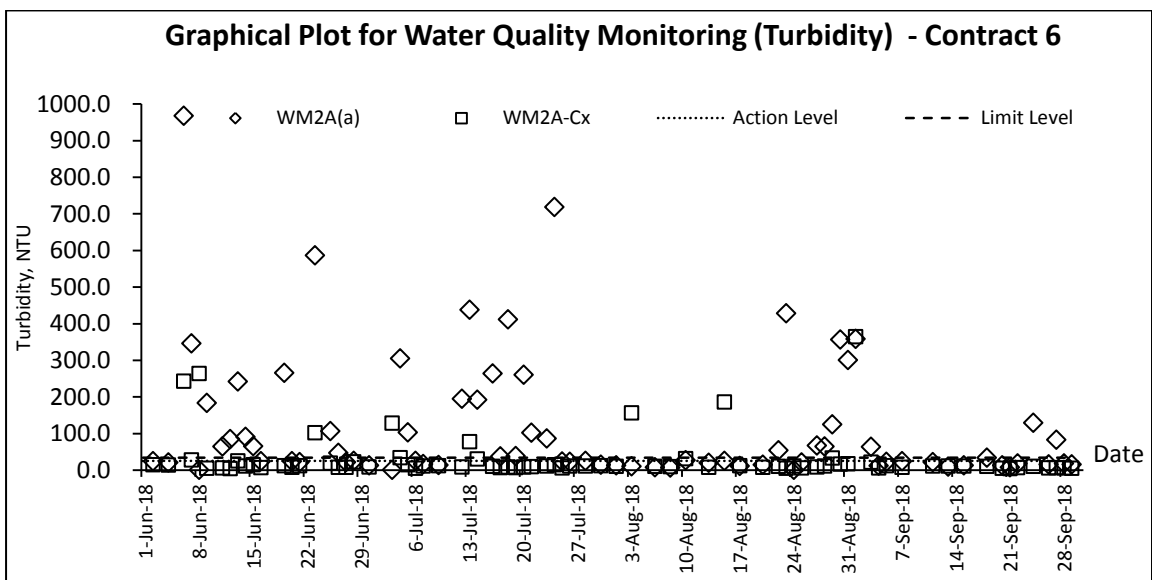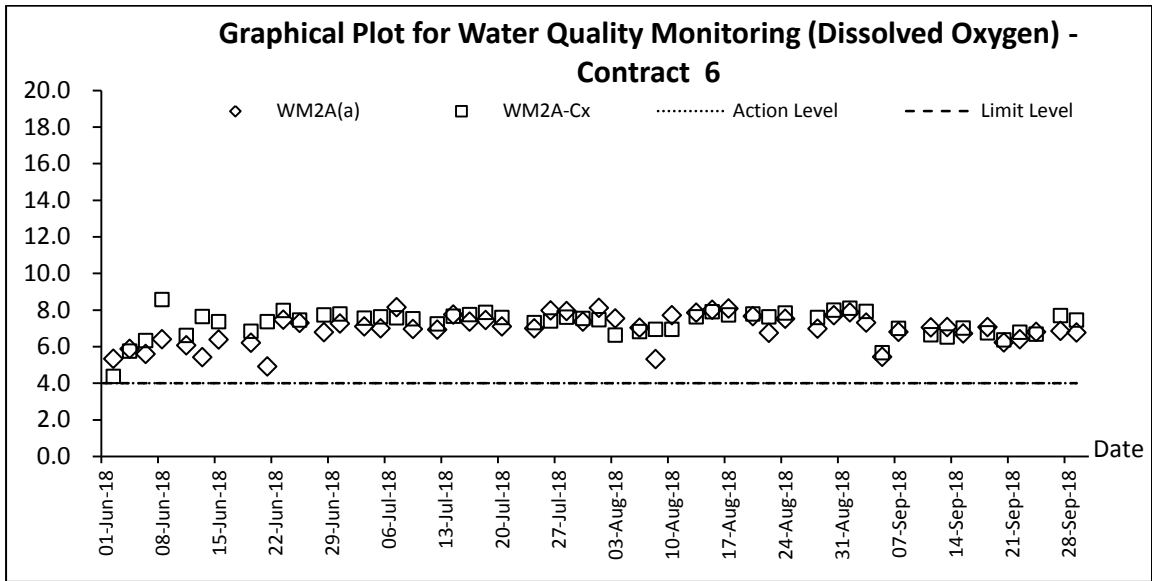

Appendix K

Meteorological Data

Date		Weather	Total Rainfall (mm)	Ta Kwu Ling Station			
				Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction
1-Sep-18	Sat	Mainly cloudy with a few showers and isolated thunderstorms.	32	26	6.0	83	SE
2-Sep-18	Sun	Mainly cloudy with isolated showers	9.8	27.3	5.5	84	S/SE
3-Sep-18	Mon	Hot with sunny periods during the day tomorrow.	0.3	27.7	6.5	80.7	E/SE
4-Sep-18	Tue	Mainly fine and hot,	0	28.9	6	77.2	W/SW
5-Sep-18	Wed	Very hot. Sunny periods with isolated showers and thunderstorms.	0.1	30	12.3	77.7	S/SW
6-Sep-18	Thu	Very hot with sunny periods and a few showers.	0	29.3	6.8	81.2	E/NE
7-Sep-18	Fri	Hot with sunny periods.	Trace	29.6	7.5	79.2	E/SE
8-Sep-18	Sat	Very hot with sunny periods and a few showers.	24.6	27.7	7.1	81.1	E
9-Sep-18	Sun	Mainly cloudy. Sunny intervals and isolated showers in the afternoon	16.7	27.2	6	73.7	E/NE
10-Sep-18	Mon	Sunny periods. Isolated showers in the afternoon. Moderate easterly winds.	0.2	26	5.6	78.7	E/NE
11-Sep-18	Tue	Mainly fine but hazy. Hot during the day. Moderate northerly winds.	0	27.4	6.5	68.7	N/NW
12-Sep-18	Wed	Mainly cloudy with a few squally showers. Showers will be more frequent with thunderstorms at first.	Trace	28.8	9.5	73	E/NE
13-Sep-18	Thu	Mainly cloudy with showers. Isolated squally thunderstorms at first.	167.5	28.5	8.4	78.7	E/NE
14-Sep-18	Fri	Mainly cloudy with showers. Isolated squally thunderstorms at first.	0	29.5	6	75.7	N/NW
15-Sep-18	Sat	Mainly fine but hazy. Hot during the day. Moderate northerly winds.	Trace	30	11	50.5	N
16-Sep-18	Sun	occasionally strong on high ground at first	167.5	27.8	37	90	E/SE
17-Sep-18	Mon	Mainly fine. Moderate to fresh east to southeasterly winds	12	28.5	17.2	78.5	E/SE
18-Sep-18	Tue	Mainly fine. Moderate to fresh east to southeasterly winds	1.2	28.6	11	77.5	E
19-Sep-18	Wed	Fine and hot. Light winds.	0	28.4	5.5	76	SW
20-Sep-18	Thu	Sunny periods. Isolated showers later. Light winds.	0	29.4	4.7	75.7	S/SW
21-Sep-18	Fri	Fine. Very hot in the afternoon. Light winds.	Trace	29.4	5.5	70.7	S/SW
22-Sep-18	Sat	Fine and hot. Light winds.	0	29.7	5.6	69.1	SW
23-Sep-18	Sun	Sunny periods. Isolated showers later. Light winds.	Trace	29.5	9.6	74.7	E/SE
24-Sep-18	Mon	Mainly cloudy with occasional showers and thunderstorms.	72.2	27.4	9.7	83.2	E/SE
25-Sep-18	Tue	Mainly cloudy with one or two showers. Sunny periods tomorrow.	34.5	27.8	6.5	75	E/SE
26-Sep-18	Wed	Mainly cloudy with one or two showers. Sunny periods tomorrow.	9.7	26.5	4.5	82	S/SW
27-Sep-18	Thu	Fine and hot. Light winds.	Trace	Maintenance	5	Maintenance	E
28-Sep-18	Fri	Mainly fine. Dry in the afternoon. Moderate northerly winds.	0	26.7	9	76.5	N
29-Sep-18	Sat	Fine. Very hot in the afternoon. Light winds.	0	27.4	10.0	76.1	SW
30-Sep-18	Sun	Mainly fine and dry. Moderate east to northeasterly winds.	0	27	8	68.5	N

Appendix L

Waste Flow Table

APPENDIX G: MONTHLY SUMMARY WASTE FLOW TABLE

FOR: 2018

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill*	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse#
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000m ³)
Jan	86.6400	0.0000	0.0000	5.2900	81.3500	1.6570	45.0000	0.3100	2.8000	4.5760	0.6575
Feb	33.2700	0.0000	0.0000	3.6700	29.6000	1.3470	32.0000	0.2500	2.4000	1.9500	0.2850
Mar	39.7600	0.0000	0.0000	3.4600	36.3000	1.3380	36.0000	0.3050	2.7000	9.8560	0.6290
Apr	55.5979	0.0000	0.0000	3.3680	52.2299	1.2470	33.7800	0.3240	2.5000	0.0000	0.5748
May	12.9815	0.0000	0.0000	4.6780	8.3035	1.1470	30.1400	0.3040	2.6000	44.9600	0.7056
June	9.0720	0.0000	0.0000	3.1910	5.8810	1.2200	31.7800	0.2870	2.3000	0.1760	0.7534
Sub-total	237.3214	0.0000	0.0000	23.6570	213.6644	7.9560	208.7000	1.7800	15.3000	61.5180	3.6053
July	6.0440	0.0000	0.0000	0.5840	5.4600	1.4570	30.7500	0.2750	2.1000	1.5840	0.8810
Aug	5.4100	0.0000	0.0000	0.7600	4.6500	1.3520	31.5900	0.2570	2.2000	3.0800	0.8400
Sep	8.0550	0.0000	0.0000	2.8300	5.2250	1.2300	30.7800	0.2200	1.8000	1.2300	0.4440
Oct	0.0000										
Nov	0.0000										
Dec	0.0000										
Sub-total	19.5090	0.0000	0.0000	4.1740	15.3350	4.0390	93.1200	0.7520	6.1000	5.8940	2.1650
Total	256.8304	0.0000	0.0000	27.8310	228.9994	11.9950	301.8200	2.5320	21.4000	67.4120	5.7703

Notes:

- (1) The performance targets are given in PS 1.100(14)(a)
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the amount of C&D materials.
- (5) Assumption: 1m³ of inert material weight 2.2 tonne 1m³ of non-inert material weight 1.6 tonne 1m³ of chemical waste weight 0.88 tonne

Monthly Summary Waste Flow Table for 2018 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in m ³)	(in '000m ³)
Jan	3.089	0.304	0.060	0.000	2.725	0.923	0.000	0.000	0.000	0.000	0.150
Feb	2.697	0.256	0.150	0.000	2.292	1.144	0.000	0.000	0.000	0.000	0.095
Mar	1.524	0.141	0.120	0.000	1.263	0.211	0.000	0.000	0.000	0.000	0.085
Apr	2.880	0.786	0.360	0.000	1.734	0.788	0.000	0.000	0.000	0.000	0.125
May	1.164	0.290	0.101	0.000	0.773	0.185	0.000	0.000	0.000	0.000	0.150
Jun	0.862	0.082	0.515	0.000	0.265	0.000	0.000	0.000	0.000	0.000	0.110
Sub-total	12.216	1.859	1.306	0.000	9.051	3.251	0.000	0.000	0.000	0.000	0.715
Jul	1.520	0.261	0.476	0.000	0.783	0.039	0.000	0.000	0.000	0.000	0.135
Aug	2.372	0.478	0.613	0.000	1.281	0.193	0.000	0.000	0.000	0.000	0.095
Sep	1.709	0.361	0.381	0.000	0.967	0.272	0.000	0.000	0.000	0.000	0.150
Oct											
Nov											
Dec											
Total	17.817	2.959	2.776	0.000	12.082	3.755	0.000	0.000	0.000	0.000	1.095

- Note:**
1. Assume the density of soil fill is 2 ton/m³.
 2. Assume the density of rock and broken concrete is 2.5 ton/m³.
 3. Assume each truck of C&D wastes is 5m³.
 4. The inert C&D materials except slurry and bentonite are disposed at Tuen Mun 38.
 5. The slurry and bentonite are disposed at Tseung Kwun O 137.
 6. The non-inert C&D wastes are disposed at NENT.
 7. Assume the density of metal is 7,850 kg/m³.
 8. Assume the density of plastic is 941 kg/m³.
 9. Assume the density of paper is 800 kg/m³.

Name of Department: CEDD

Contract No.: NE/2014/02

Monthly Summary Waste Flow Table for 2018

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2016	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2017	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jan-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Feb-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jun-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jul-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Aug-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sep-18	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Oct-18											
Nov-18											
Dec-18											
Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000

Forecast of Total Quantities of C&D Materials to be Generated from the Contract*										
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
0.500	0.000	0.000	0.000	0.500	0.000	0.500	0.200	0.000	0.000	0.200

Notes :

- (1) The performance targets are given in PS Clause 1.84(14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Sites.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- (4) Estimate 6m³ capacity per dump truck

Monthly Summary Waste Flow Table for 2018 (year)

Name of Person completing the record: K.M. Lui (EO)

Project : Liangtang / Heung Yuen Wai Boundary Control Point Site Formation and Infrastructure Works – Contract 6

Contract No.: CV/2013/08

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Jan	4.152	0	0.629	1.947	1.576	0	0	0.240	0	0	0.892
Feb	2.740	0	0.867	0.544	1.329	0	0	0.402	0	0	0.578
Mar	3.269	0	1.581	0.969	0.719	0	0	0.380	0	0	0.725
Apr	2.901	0	0.255	1.955	0.691	0	0	0.360	0	0	0.921
May	3.194	0	0.068	1.964	1.162	0	0	0.384	0	0	1.340
Jun	2.206	0	0	0.9775	1.228	0	0	0.270	0	0	0.714
Sub-total	18.462	0.000	3.400	8.357	6.705	0.000	0.000	2.036	0.000	0.000	5.170
Jul	1.512	0	0	0.816	0.696	0	0	1.608	0	0	0.846
Aug	2.562	0	0	1.989	0.573	0	0	0.360	0	0	0.866
Sep	0.997	0	0	0.552	0.445	0	0	0.225	0	0	0.633
Oct											
Nov											
Dec											
Total	1021.926	0.000	166.627	282.357	572.944	53.939	0.000	10.608	0.007	34.045	16.266

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (2) Plastics refer to plastic bottles/containers, plastic sheets/ foam from packaging materials.
 - (3) Broken concrete for recycling into aggregates.

MONTHLY SUMMARY WASTE FLOW TABLEName of Department: CEDD Contract Title: Liantang/ Heung Yuen Wai Boundary Control Point
Site Formation and Infrastructure Works – Contract 7Contract No.: NE/2014/03 **Monthly Summary Waste Flow Table for 2018 (year)**

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-Inert C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/cardboard packaging	Plastic (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	0.015	0	0	0	0.015	0	14.5	0.5	0.001	0	0.15
Feb	0	0	0	0	0	0	9	0.18	0.001	0	0.13
Mar	0.005	0	0	0	0.005	0	6	0.15	0.001	0	0.2
Apr	1.1	0	0	0	1.1	0	6.6	0.22	0.001	0	0.3
May	0.077	0	0	0	0.077	0	1.3	0.15	0.001	0	0.1
June	0	0	0	0	0	0	6	0.4	0.001	0	0.05
Sub-total	1.197	0	0	0	1.197	0	43.4	1.6	0.006	0	0.93
July	0.5	0	0	0	0.5	0	2.5	0.1	0.001	0	0.2
Aug	0.047	0	0	0	0.047	0	5.8	0.1	0.001	0	0.1
Sept	0.041	0	0	0	0.041	0	1.1	0.1	0.001	0	0.1
Oct											
Nov											
Dec											
Total	1.785	0	0	0	1.785	0	52.8	1.9	0.009	0	1.330

Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
(2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

Contract No. / Works Order No.: - SSC505**Monthly Summary Waste Flow Table for 2018** [year] [to be submitted not later than the 15th day of each month following reporting month]

(All quantities shall be rounded off to 3 decimal places.)

Month	Actual Quantities of Inert Construction Waste Generated Monthly				
	(a)=(b)+(c)+(d)+(e) Total Quantity Generated	(b) Broken Concrete (see Note 4)	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)
Jan	5.298	0.646	0.160	0.000	4.492
Feb	7.243	0.572	0.320	0.000	6.351
Mar	11.241	0.831	0.225	0.000	10.186
Apr	3.717	1.458	0.257	0.000	2.002
May	5.346	0.788	0.300	0.000	4.258
Jun	6.828	0.661	0.376	0.000	5.792
Sub-total	39.672	4.956	1.638	0.000	33.079
Jul	11.637	0.051	0.282	0.000	11.304
Aug	16.440	0.142	0.263	0.000	16.036
Sep	7.849	0.116	0.161	0.000	7.573
Oct					
Nov					
Dec					
Total	75.598	5.265	2.344	0.000	67.990

Month	Actual Quantities of Non-inert Construction Waste Generated Monthly												
	Timber		Metals		Paper/ cardboard packaging		Plastics (see Note 3)		Chemical Waste		Other Recyclable Materials (see Page 3)		General Refuse disposed of at Landfill
	(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000m ³)
	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated
Jan	0.000	0.000	375.870	375.870	0.220	0.220	0.032	0.032	0.000	0.000	0.000	0.000	1.918
Feb	0.000	0.000	720.120	720.120	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.223
Mar	0.000	0.000	220.860	220.860	0.830	0.830	0.005	0.005	0.000	0.000	0.005	0.005	2.711
Apr	0.000	0.000	202.130	202.130	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.470
May	0.000	0.000	294.330	294.330	0.000	0.000	0.042	0.042	0.000	0.000	0.000	0.000	2.490
Jun	0.000	0.000	242.170	242.170	0.990	0.990	0.000	0.000	1.200	0.000	0.000	0.000	2.997
Sub-total	0.000	0.000	2,055.480	2,055.480	2.040	2.040	0.079	0.079	1.200	0.000	0.005	0.005	14.809
Jul	0.000	0.000	218.990	218.990	0.280	0.280	0.000	0.000	0.000	0.000	0.000	0.000	3.146
Aug	0.000	0.000	466.220	466.220	0.230	0.230	0.000	0.000	1.200	0.000	0.000	0.000	3.114
Sep	0.000	0.000	153.620	153.620	0.620	0.620	0.033	0.033	0.000	0.000	0.000	0.000	2.704
Oct													
Nov													
Dec													
Total	0.000	0.000	2,894.310	2,894.310	3.170	3.170	0.112	0.112	2.400	0.000	0.005	0.005	23.773

Appendix M

**Implementation Schedule for
Environmental Mitigation Measures**

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
Air Quality Impact (Construction)							
3.6.1.1	2.1	<p>General Dust Control Measures</p> <p>The following dust suppression measures should be implemented:</p> <ul style="list-style-type: none"> ■ Frequent water spraying for active construction areas (4 times per day for active areas in Po Kak Tsai and 8 times per day for all other active areas), including areas with heavy construction and slope cutting activities ■ 80% of stockpile areas should be covered by impervious sheets ■ Speed of trucks within the site should be controlled to about 10 km/hr ■ All haul roads within the site should be paved to avoid dust emission due to vehicular movement 	To minimize adverse dust emission generated from various construction activities of the works sites	Contractor	Construction Works Sites	During Construction	EIA Recommendation and Air Pollution Control (Construction Dust) Regulation
3.6.1.2	2.1	<p>Best Practice for Dust Control</p> <p>The relevant best practices for dust control as stipulated in the Air Pollution Control (Construction Dust) Regulation should be adopted to further reduce the construction dust impacts of the Project. These best practices include:</p> <p><i>Good site management</i></p> <ul style="list-style-type: none"> ■ The Contractor should maintain high standard of housekeeping to prevent emission of fugitive dust. ■ Loading, unloading, handling and storage of raw materials, wastes or by-products should be carried out in a manner so as to minimize the release of visible dust emission. ■ Any piles of materials accumulated on or around the work areas should be cleaned up regularly. ■ Cleaning, repair and maintenance of all plant facilities within the work areas should be carried out in a manner minimizing generation of fugitive dust emissions. ■ The material should be handled properly to prevent fugitive dust emission before cleaning. <p><i>Disturbed Parts of the Roads</i></p> <ul style="list-style-type: none"> ■ Each and every main temporary access should be paved with 	To minimize adverse dust emission generated from various construction activities of the works sites	Contractor	Construction Works Sites	During Construction	EIA Recommendation and Air Pollution Control (Construction Dust) Regulation

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials; or</p> <ul style="list-style-type: none"> Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet. <p><i>Exposed Earth</i></p> <ul style="list-style-type: none"> Exposed earth should be properly treated by compaction, hydroseeding, vegetation planting or seeding with latex, vinyl, bitumen within six months after the last construction activity on the site or part of the site where the exposed earth lies. <p><i>Loading, Unloading or Transfer of Dusty Materials</i></p> <ul style="list-style-type: none"> All dusty materials should be sprayed with water immediately prior to any loading or transfer operation so as to keep the dusty material wet. <p><i>Debris Handling</i></p> <ul style="list-style-type: none"> Any debris should be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the three sides. Before debris is dumped into a chute, water should be sprayed so that it remains wet when it is dumped. <p><i>Transport of Dusty Materials</i></p> <ul style="list-style-type: none"> Vehicle used for transporting dusty materials/spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards. <p><i>Wheel washing</i></p> <ul style="list-style-type: none"> Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. <p><i>Use of vehicles</i></p> <ul style="list-style-type: none"> Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. Where a vehicle leaving the construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle. 					

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p><i>Site hoarding</i></p> <ul style="list-style-type: none"> Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit. <p><i>Blasting</i></p> <ul style="list-style-type: none"> The areas within 30m from the blasting area should be wetted with water prior to blasting. 					
<u>Air Quality Impact (Operation)</u>							
3.5.2.2	2.2	<p>The following odour containment and control measures will be provided for the proposed sewage treatment work at the BCP site:</p> <ul style="list-style-type: none"> The treatment work will be totally enclosed. Negative pressure ventilation will be provided within the enclosure to avoid any fugitive odorous emission from the treatment work. Further odour containment will be achieved by covering or confining the sewage channels, sewage tanks, and equipment with potential odour emission. Proper mixing will be provided at the equalization and sludge holding tanks to prevent sewage septicity. Chemical or biological deodorisation facilities with a minimum odour removal efficiency of 90% will be provided to treat potential odorous emissions from the treatment plant including sewage channels / tanks, filter press and screening facilities so as to minimize any potential odour impact to the nearby ASRs. 	To minimize potential odour impact from operation of the proposed sewage treatment work at BCP	DSD	BCP	Operation Phase	EIA recommendation
<u>Noise Impact (Construction)</u>							
4.4.1.4	3.1	<p>Adoption of Quieter PME</p> <p>Use of the recommended quieter PME such as those given in the BS5228: Part 1:2009 and presented in Table 4.14, which can be found in Hong Kong.</p>	To minimize the construction air-borne noise impact	Contractors	Construction Work Sites	During Construction	EIA recommendation, EIAO and Noise Control Ordinance (NCO)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
4.4.1.4	3.1	<p>Use of Movable Noise Barrier</p> <p>The use of movable barrier for certain PME can further alleviate the construction noise impacts. In general, a 5 dB(A) reduction for movable PME and 10 dB(A) for stationary PME can be achieved depending on the actual design of the movable noise barrier. The Contractor shall be responsible for design of the movable noise barrier with due consideration given to the size of the PME and the requirement for intercepting the line of sight between the NSRs and PME. Barrier material with surface mass in excess of 7 kg/m² is recommended to achieve the predicted screening effect.</p>	To minimize the construction air-borne noise impact	Contractors	Construction Work Sites	During Construction	EIA recommendation, EIAO and NCO
4.4.1.4	3.1	<p>Use of Noise Enclosure/ Acoustic Shed</p> <p>The use of noise enclosure or acoustic shed is to cover stationary PME such as air compressor and concrete pump. With the adoption of the noise enclosure, the PME could be completely screened, and noise reduction of 15 dB(A) can be achieved according to the GW-TM.</p>	To minimize the construction air-borne noise impact	Contractors	Construction Work Sites	During Construction	EIA recommendation, EIAO and NCO
4.4.1.4	3.1	<p>Use of Noise Insulating Fabric</p> <p>Noise insulating fabric can be adopted for certain PME (e.g. drill rig, pilling auger etc). The insulating fabric should be lapped such that there are no openings or gaps on the joints. Technical data from manufacturers state that by using the Fabric, a noise reduction of over 10 dB(A) can be achieved on noise level.</p>	To minimize the construction air-borne noise impact	Contractors	Construction Work Sites	During Construction	EIA recommendation, EIAO and NCO

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
4.4.1.4	3.1	<p>Good Site Practice</p> <p>The good site practices listed below should be followed during each phase of construction:</p> <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; • Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction programme; • Mobile plant, if any, should be sited as far from NSRs as possible; • Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and • Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	To minimize the construction air-borne noise impact	Contractors	Construction Work Sites	During Construction	EIA recommendation, EIAO and NCO
<u>Noise Impact (Operation)</u>							
<u>Road Traffic Noise</u>							
Table 4.42 and Figure 4.20.1 to 4.20.4	3.2	Erection of noise barrier/ enclosure along the viaduct section.	To minimize the road traffic noise along the connecting road of BCP	Contractor	Loi Tung and Fanling Highway Interchange	Before Operation	EIAO and NCO
<u>Fixed Plant Noise</u>							
Table 4.46	3.2	Specification of the maximum allowable sound power levels of the proposed fixed plants during daytime and night-time.	To minimize the fixed plant noise impact	Managing Authority of the buildings / Contractor	BCP, Administration Building and all ventilation buildings	Before Operation	EIA recommendation, EIAO and NCO

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
4.5.2.4	3.2	<p>The following noise reduction measures shall be considered as far as practicable during operation:</p> <ul style="list-style-type: none"> Choose quieter plant such as those which have been effectively silenced; Include noise levels specification when ordering new plant (including chillier and E/M equipment); Locate fixed plant/louver away from any NSRs as far as practicable; Locate fixed plant in walled plant rooms or in specially designed enclosures; Locate noisy machines in a basement or a completely separate building; Install direct noise mitigation measures including silencers, acoustic louvers and acoustic enclosure where necessary; and Develop and implement a regularly scheduled plant maintenance programme so that equipment is properly operated and serviced in order to maintain a controlled level of noise. 	To minimize the fixed plant noise impact	Managing Authority of the buildings / Contractor	BCP, Administration Building and all ventilation buildings	Before Operation	EIAO and NCO
Water Quality Impact (Construction)							
5.6.1.1	4.1	<p>Construction site runoff and drainage</p> <p>The site practices outlined in ProPECC Note PN 1/94 should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. The following measures are recommended to protect water quality and when properly implemented should be sufficient to adequately control site discharges so as to avoid water quality impacts:</p> <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system should be undertaken by the Contractor prior to the commencement of construction. The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. 	To control site runoff and drainage; prevent high sediment loading from reaching the nearby watercourses	Contractor	Construction Works Sites	Construction Phase	Practice Note for Professional Persons on Construction Site Drainage (ProPECC Note PN 1/94)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>Temporary ditches should be provided to facilitate the runoff discharge into stormwater drainage system through a sediment/silt trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates, if practical.</p> <ul style="list-style-type: none"> ▪ Sand/silt removal facilities such as sand/silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC Note PN 1/94. Sizes may vary depending upon the flow rate. The detailed design of the sand/silt traps should be undertaken by the Contractor prior to the commencement of construction. ▪ All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. ▪ Measures should be taken to minimize the ingress of site drainage into excavations. If excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities. ▪ If surface excavation works cannot be avoided during the wet season (April to September), temporarily exposed slope/soil surfaces should be covered by tarpaulin or other means, as far as practicable, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Interception channels should be provided (e.g. along the crest/edge of the excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place to ensure that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC Note PN 1/94. ▪ The overall slope of the site should be kept to a minimum to reduce 					

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>the erosive potential of surface water flows.</p> <ul style="list-style-type: none"> ▪ All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facility should be provided at construction site exit where practicable. Wash-water should have sand and silt settled out and removed regularly to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. ▪ Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. ▪ Manholes (including newly constructed ones) should be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and stormwater runoff being directed into foul sewers. ▪ Precautions should be taken at any time of the year when rainstorms are likely. Actions should be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC Note PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. ▪ Bentonite slurries used in piling or slurry walling should be reconditioned and reused wherever practicable. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after all the related construction activities are completed. The requirements in ProPECC Note PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 					
5.6.1.1	4.1	<p>Good site practices for works within water gathering grounds</p> <p>The following conditions should be complied, if there is any works to be carried out within the water gathering grounds:</p>	To minimize water quality impacts to the water gathering grounds	Contractor	Construction Works Sites within the water gathering	Construction Phase	ProPECC Note PN 1/94

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<ul style="list-style-type: none"> ▪ Adequate measures should be implemented to ensure no pollution or siltation occurs to the catchwaters and catchments. ▪ No earth, building materials, oil or fuel, soil, toxic materials or any materials that may possibly cause contamination to water gathering grounds are allowed to be stockpiled on site. ▪ All surplus spoil should be removed from water gathering grounds as soon as possible. ▪ Temporary drains with silt traps should be constructed at the site boundary before the commencement of any earthworks. ▪ Regular cleaning of silt traps should be carried out to ensure proper operation at all time. ▪ All excavated or filled surfaces which have the risk of erosion should always be protected form erosion. ▪ Facilities for washing the wheels of vehicles before leaving the site should be provided. ▪ Any construction plant which causes pollution to catchwaters or catchments due to the leakage of oil or fuel should be removed off site immediately. ▪ No maintenance activities which may generate chemical wastes should be undertaken in the water gathering grounds. Vehicle maintenance should be confined to designated paved areas only and any spillages should be cleared up immediately using absorbents and waste oils should be collected in designated tanks prior to disposal off site. All storm water run-off from these areas should be discharged via oil/petrol separators and sand/silt removal traps. ▪ Any soil contaminated with fuel leaked from plant should be removed off site and the voids arising from removal of contaminated soil should be replaced by suitable material approved by the Director of Water Supplies. ▪ Provision of temporary toilet facilities and use of chemicals or insecticide of any kind are subject to the approval of the Director of Water Supplies. ▪ Drainage plans should be submitted for approval by the Director of 			grounds		

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>Water Supplies.</p> <ul style="list-style-type: none"> ▪ An unimpeded access through the waterworks access road should always be maintained. ▪ Earthworks near catchwaters or streamcourses should only be carried out in dry season between October and March, ▪ Advance notice must be given before the commencement of works on site quoting WSD's approval letter reference. 					
5.6.1.2	4.1	<p>Good site practices of general construction activities</p> <p>Construction solid waste, debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby stormwater drain. Stockpiles of cement and other construction materials should be kept covered when not being used.</p> <p>Oils and fuels should only be stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to any nearby stormwater drain, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event.</p>	To minimize water quality impacts	Contractor	All construction works sites	Construction phase	EIA Recommendation
5.6.1.3	4.1	<p>Sewage effluent from construction workforce</p> <p>Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.</p>	To minimize water quality impacts	Contractor	All construction works sites with on-site sanitary facilities	Construction phase	EIA Recommendation and Water Pollution Control Ordinance (WPCO)
5.6.1.4	4.1	<p>Hydrogeological Impact</p> <p>Grout injection works would be conducted before blasting, for sealing a limited area around the tunnel with a grout of a suitable strength for controlling the potential groundwater inflows. The pre-injection grouting method would be supplemented by post-injection grouting where necessary to further enhance the groundwater inflow control. On-site treatment for the groundwater ingress pumped out would be required to remove any contamination by grouting materials before discharge off-site.</p>	To minimize water quality impacts	Contractor	Construction works sites of the drill and blast tunnel	Construction phase	EIA Recommendation and WPCO
Water Quality Impact (Operation)							
No mitigation measure is required.							

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
<u>Sewage and Sewerage Treatment Impact (Construction)</u>							
6.7	5	The sewage generated by the on-site workforce should be collected in chemical toilets and disposed of off-site by a licensed waste collector.	To minimize water quality impacts	Contractor	All construction works sites with on-site sanitary facilities	Construction phase	EIA recommendation and WPCO
<u>Sewage and Sewerage Treatment Impact (Operation)</u>							
6.6.3	5	Sewage generated by the BCP and Chuk Yuen Village Resite will be collected and treated by the proposed on-site sewage treatment facility using Membrane Bioreactor treatment with a portion of the treated wastewater reused for irrigation and flushing within the BCP.	To minimize water quality impacts	DSD	BCP	Operation phase	EIA recommendation and WPCO
6.5.3	5	Sewage generated from the Administration Building will be discharged to the existing local sewerage system.	To minimize water quality impacts	DSD	Administration Building	Operation phase	EIA recommendation and WPCO
<u>Waste Management Implication (Construction)</u>							
7.6.1.1	6	<p>Good Site Practices</p> <p>Adverse impacts related to waste management such as potential hazard, air, odour, noise, wastewater discharge and public transport as mentioned in section 3.4.7.2 (ii)(c) of the Study Brief are not expected to arise, provided that good site practices are strictly followed. Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> ▪ Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site ▪ Training of site personnel in proper waste management and chemical handling procedures ▪ Provision of sufficient waste disposal points and regular collection of waste ▪ Dust suppression measures as required under the Air Pollution Control (Construction Dust) Regulation should be followed as far as practicable. Appropriate measures to minimise windblown litter and dust/odour during transportation of waste by covering trucks or in enclosed containers ▪ General refuse shall be removed away immediately for disposal. As 	To minimize adverse environmental impact	Contractor	Construction works sites (general)	Construction Phase	EIA recommendation; Waste Disposal Ordinance; Waste Disposal (Chemical Wastes) (General) Regulation; and ETWB TC(W) No. 19/2005, Environmental Management on Construction Site

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>such odour is not anticipated to be an issue to distant sensitive receivers</p> <ul style="list-style-type: none"> ▪ Provision of wheel washing facilities before the trucks leaving the works area so as to minimise dust introduction from public road ▪ Covers and water spraying system should be provided for the stockpiled C&D material to prevent dust impact or being washed away ▪ Designate different locations for storage of C&D material to enhance reuse ▪ Well planned programme for transportation of C&D material to lessen the off-site traffic impact. Well planned delivery programme for offsite disposal and imported filling material such that adverse noise impact from transporting of C&D material is not anticipated ▪ Site practices outlined in ProPECC PN 1/94 “Construction Site Drainage” should be adopted as far as practicable, such as cleaning and maintenance of drainage systems regularly ▪ Provision of cover for the stockpile material, sand bag or earth bund as barrier to prevent material from washing away and entering the drains 					
7.6.1.2	6	<p>Waste Reduction Measures</p> <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> ▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal ▪ Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force ▪ Proper storage and site practices to minimise the potential for damage or contamination of construction materials ▪ Plan and stock construction materials carefully to minimise amount 	To reduce the quantity of wastes	Contractor	Construction works sites (General)	Construction Phase	EIA recommendation and Waste Disposal Ordinance

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
		<p>of waste generated and avoid unnecessary generation of waste</p> <ul style="list-style-type: none"> In addition to the above measures, specific mitigation measures are recommended below for the identified waste arising to minimise environmental impacts during handling, transportation and disposal of these wastes. 					
7.6.1.3	6	<p>C&D Materials</p> <p>In order to minimise impacts resulting from collection and transportation of C&D material for off-site disposal, the excavated materials should be reused on-site as backfilling material as far as practicable. The surplus rock and other inert C&D material would be disposed of at the Government's Public Fill Reception Facilities (PFRFs) at Tuen Mun Area 38 for beneficial use by other projects in the HKSAR as the last resort. C&D waste generated from general site clearance and tree felling works would require disposal to the designated landfill site. Other mitigation requirements are listed below:</p> <ul style="list-style-type: none"> A Waste Management Plan should be prepared and implemented in accordance with ETWB TC(W) No. 19/2005 Environmental Management on Construction Site; and In order to monitor the disposal of C&D material and solid wastes at public filling facilities and landfills, and to control fly-tipping, a trip-ticket system (e.g. ETWB TCW No. 31/2004) should be included. 	To minimize impacts resulting from C&D material	Contractor	Construction Works Sites (General)	Construction Phase	EIA recommendation; Waste Disposal Ordinance; and ETWB TCW No. 31/2004
7.6.1.4	6	<p>General refuse</p> <p>General refuse should be stored in enclosed bins or compaction units separated from other C&D material. A reputable waste collector is to be employed by the Contractor to remove general refuse from the site separately. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' litter.</p>	To minimize impacts resulting from collection and transportation of general refuse for off-site disposal	Contractor	Construction works sites (General)	Construction phase	Waste Disposal Ordinance and Public Health and Municipal Services Ordinance - Public Cleansing and Prevention of Nuisances Regulation
7.6.1.5	6	<p>Chemical waste</p> <p>If chemical wastes are produced at the construction site, the Contractor will be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the <i>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</i>. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical</p>	To minimize impacts resulting from collection and transportation of chemical waste for off-site disposal	Contractor	Construction works sites (General)	Construction phase	Waste Disposal (Chemical Waste) (General) Regulation and Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes

Appendix N

Investigation Report for Exceedance

Agreement No. CE 45/2008
Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works
Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008	
Date		30 August 2018	
Location		WM1	
Time		10:20	
Parameter		Turbidity (NTU)	Suspended Solids (mg/L)
Action Level		51.3 AND 120% of upstream control station of the same day	54.5 AND 120% of upstream control station of the same day
Limit Level		67.6 AND 130% of upstream control station of the same day	64.9 AND 130% of upstream control station of the same day
Measured Levels	WM1-C	369.5	319.0
	WM1	Over Range	626.5
Exceedance		Limit Level	Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided from CCKJV, construction activities carried out on 30 August 2018 at Bridge Y (near WM1) include construction of retaining wall and drainage system at Bridge Y. The monitoring locations and works area are shown in <i>Figure 1</i>. 2. According to the field photos taken on 30 August 2018, muddy water was observed throughout the river channel including impact station WM1 and control station WM1-C. (Photos 1 to 2) 3. According to the weather information from the Observatory, there was heavy rainstorm with total rainfall of 71.6mm and 23.3mm record on 28 and 29 August 2018 respectively. The water quality throughout the river course was highly affected by the stirred up sediment and muddy runoff from the surrounding environment other than the construction site. 4. Joint site inspection was carried out by the RE, IEC, CCKJV and ET on 30 August 2018. The observation during the site inspections were summarized below. <ol style="list-style-type: none"> (a) Silt was observed along the public road near Bridge Y and CCKJV was advised to provide proper mitigation measures to avoid accumulation of silt and maintain the public road clean and tidy. (Photo 3 & Figure 1) CCKJV has removed the silt promptly after the site inspection. (Photo 4 & Figure 1) Since the silt found on the public road was not close to the stream and WM1, the water quality impact arising from the deficiency was considered neglected. (b) The pump to divert wastewater to Wetsep for treatment in Chuk Yuen Village was out of order and CCKJV was advised to replace the pump properly and ensure the wastewater was treated before discharge. There was no discharge observed from the Wetsep and no adverse water quality impact contributed to WM1 was observed. (c) Wheel washing was carried out on the paved ground to minimize the generation of muddy water. (Photo 5) 5. In our investigation, water quality mitigation implemented for Bridge Y and no adverse water quality impact contributed to WM1 was observed. Since muddy water was also observed at control station after rain, it was considered that exceedances were related to the impact of rainstorm and not due to the works under Contract 6. 6. According to the Event and Action, the monitoring frequency at WM1 has been increased to daily due to the limit level exceedance recorded 	

	until no exceedances were triggered in consecutive days. Additional monitoring was carried out on 31 August and 1 September 2018 and no exceedances were triggered. Nevertheless, the Contractor should continue fully implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.
--	--

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature : 

Date : 21 September 2018

Photo Record**Photo 1**

On 30 August 2018, muddy water was observed at WM1.

**Photo 2**

On 30 August 2018, muddy water was observed at WM1-C.

**Photo 3**

During site inspection on 30 August 2018, silt was observed along the public road near Bridge Y and CCKJV was advised to provide proper mitigation measures to avoid accumulation of silt and maintain the public road clean and tidy.

**Photo 4**

The silt was promptly removed by the Contractor after the site inspection.

**Photo 5**

Wheel washing was carried out on the paved ground to minimize the generation of muddy water.



Figure 1 Location Map for Water Quality Monitoring Locations WM1 and WM1-C

Agreement No. CE 45/2008

Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works

Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008	
Date		27 August 2018	28 August 2018
Location		WM2A(a)	
Time		14:45	10:45
Parameter		Turbidity (NTU) / Suspended solids (mg/L)	
Action Level		24.9 AND 120% of upstream control station of the same day / 14.6 AND 120% of upstream control station of the same day	
Limit Level		33.8 AND 130% of upstream control station of the same day / 17.3 AND 130% of upstream control station of the same day	
Measured Levels	WM2A-C	8.0 / 6.0	11.0 / 6.0
	WM2A(a)	66.6 / 60.0	64.2 / 51.5
Exceedance		Limit Level	Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided from the Contractor of Contract 6 (CCKJV), construction activities carried out on 27 and 28 August 2018 at Bridge D (upstream of WM2A(a)) were mainly bridge construction. The monitoring locations and work boundary are shown in <i>Figure 1</i>. 2. According to the site photo taken by the monitoring team during water sampling on 27 and 28 August 2018, turbid water was observed at impact station WM2A(a) while the water quality at WM2A-C was visually clear. (<i>Photos 1 to 4</i>) 3. According to the weather information from the Observatory, total rainfall of 80.2mm, 27.3mm and 71.6mm were recorded on 26, 27 and 28 August 2018 respectively. Under the impact of rainstorm, the water quality throughout the river channel was highly affected by the stirred up sediment and muddy runoff from the surrounding environment even outside the construction site. 4. On 27 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment. (<i>Photo 5</i>) On 28 August 2018, generation of muddy water was observed at downstream of Nylon Dam which caused by stirred up sediment when river water vertical dropped from Nylon Dam. (<i>Photo 6</i>) 5. The information and implementation of mitigation measures provided by The Contractor is summarized below. <ol style="list-style-type: none"> (a) Bridge construction work was carried out at Bridge D and there was no discharge due to nature of works. (b) Wastewater treatment facilities were properly provided for Bridge D and functioned properly. (<i>Figure 1</i>) (c) As water quality mitigation measures, open slopes were covered with tarpaulin sheet or hard paved as far as practicable to minimize muddy 	

	<p>runoff. (<i>Photos 7 & 8</i>)</p> <p>6. In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 27 and 28 August 2018 were related to the impact of rainstorm and not caused by the works under the Project.</p> <p>7. According to the Event and Action Plan, the frequency of water monitoring is increase to daily. There were turbidity and SS exceedances recorded on 29 and 30 August 2018 and another investigation will be provided. Nevertheless, the Contractor should continue implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.</p>
--	---

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature : 

Date : 24 September 2018

Photo Record



Photo 1

On 27 August 2018, turbid water was observed in WM2A(a).



Photo 2

On 27 August 2018, the water quality observed at WM2A-C was clear.



Photo 3

On 28 August 2018, turbid water was observed in WM2A(a).



Photo 4

On 28 August 2018, the water quality observed at WM2A-C was clear.



Photo 5

On 27 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment.



Photo 6

On 28 August 2018, generation of muddy water was observed at downstream of Nylon Dam caused by stirred up sediment when river water vertical dropped from Nylon Dam.



Photo 7

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Photo 8

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Figure 1 Location Map for Water Quality Monitoring Locations WM2A(a), WM2A-Control and work area under Contract 6

Agreement No. CE 45/2008

Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works

Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008		
Date		29 August 2018	30 August 2018	31 August 2018
Location		WM2A(a)		
Time		10:00	10:40	11:20
Parameter		Turbidity (NTU) / Suspended solids (mg/L)		
Action Level		24.9 AND 120% of upstream control station of the same day / 14.6 AND 120% of upstream control station of the same day		
Limit Level		33.8 AND 130% of upstream control station of the same day / 17.3 AND 130% of upstream control station of the same day		
Measured Levels	WM2A-C	32.3 / 28.0	16.3 / 13.5	16.5 / 18.0
	WM2A(a)	124.5 / 101.0	356.0 / 281.0	300.0 / 200.0
Exceedance		Limit Level	Limit Level	Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided from the Contractor of Contract 6 (CCKJV), construction activities carried out on 29 to 31 August 2018 at Bridge D (upstream of WM2A(a)) were mainly bridge construction. The monitoring locations and work boundary are shown in <i>Figure 1</i>. 2. According to the site photo taken by the monitoring team during water sampling on 29, 30 and 31 August 2018, muddy water was observed at impact station WM2A(a) while the water quality at WM2A-C appeared slightly turbid. (<i>Photos 1 to 6</i>) The water flow of the river course was relatively rapid under rainy condition. 3. According to the weather information from the Observatory, Amber Rainstorm Warning Signal, Red Rainstorm Warning Signal and Landslip Warning were issued by the Observatory on 29 August 2018. Moreover, special announcement on flooding in the northern New Territories was in force during 29 and 30 August 2018. Under the influence of continuous rainstorm, the water quality of river course was inevitably be affected by the stirred up sediment and erosion from the surrounding environment even outside the construction site. 4. During water quality monitoring on 29, 30 and 31 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment. (<i>Photos 7 to 9</i>) 5. The information and implementation of mitigation measures provided by The Contractor is summarized below. <ol style="list-style-type: none"> (a) Bridge construction work was carried out at Bridge D and there was no discharge due to nature of works. (b) Generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment. (<i>Photo 10</i>) 		

	<p>(c) Wastewater treatment facilities were properly provided for Bridge D and functioned properly. (<i>Figure 1</i>)</p> <p>(d) As water quality mitigation measures, open slopes were covered with tarpaulin sheet or hard paved as far as practicable to minimize muddy runoff. (<i>Photos 11 & 12</i>)</p> <p>6. In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 29 to 31 August 2018 were related to the impact of rainstorm and not caused by the works under the Project.</p> <p>7. According to the Event and Action Plan, the frequency of water monitoring is increased to daily. There were turbidity and SS exceedances recorded on 3 September 2018 and another investigation will be provided. Nevertheless, the Contractor should continue implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.</p>
--	--

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature :



Date : 24 September 2018

Photo Record



Photo 1

On 29 August 2018, muddy water was observed in WM2A(a).



Photo 2

On 29 August 2018, the water quality at WM2A-C appeared slightly turbid.



Photo 3

On 30 August 2018, muddy water was observed in WM2A(a).



Photo 4

On 30 August 2018, the water quality at WM2A-C appeared slightly turbid.



Photo 5

On 31 August 2018, muddy water was observed in WM2A(a).



Photo 6

On 31 August 2018, the water quality at WM2A-C appeared slightly turbid.



Photo 7

On 29 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment.



Photo 8

On 30 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment.



Photo 9

On 31 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment.



Photo 10

During site inspection on 30 August 2018, generation of muddy water was observed during deflation of Nylon Dam and the rapid water flow stirred up the loose sediment.



Photo 11

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Photo 12

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Figure 1 Location Map for Water Quality Monitoring Locations WM2A(a), WM2A-Control and work area under Contract 6

Agreement No. CE 45/2008

Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works

Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008
Date		3 September 2018
Location		WM2A(a)
Time		10:30
Parameter		Turbidity (NTU) / Suspended solids (mg/L)
Action Level		24.9 AND 120% of upstream control station of the same day / 14.6 AND 120% of upstream control station of the same day
Limit Level		33.8 AND 130% of upstream control station of the same day / 17.3 AND 130% of upstream control station of the same day
Measured Levels	WM2A-C	21.8 / 6.0
	WM2A(a)	62.9 / 65.0
Exceedance		Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided by the Contractor of Contract 6 (CCKJV), construction activities carried out on 3 September 2018 at Bridge D (upstream of WM2A(a)) were mainly bridge construction. The monitoring locations and work boundary are shown in <i>Figure 1</i>. 2. According to the site photo taken by the monitoring team on 3 September 2018, muddy water was observed at impact station WM2A(a) while the water quality at WM2A-C was clear. (<i>Photos 1 & 2</i>) 3. According to the weather information from the Observatory, Amber Rainstorm Warning Signal was issued on 2 September 2018. Under the influence of continuous rainstorm, the water quality of river course was inevitably be affected by the stirred up sediment and erosion from the surrounding environment even outside the construction site. 4. During water sampling on 1 September 2018, inflow of muddy water was observed from upstream of WM2A-C that affecting the water quality of the river course. (<i>Photo 3</i>) On 3 September 2018, it was observed that muddy water from upstream was trapped at Nylon Dam and flowing to downstream slowly. (<i>Photo 4</i>) 5. The information and implementation of mitigation measures provided by The Contractor is summarized below. <ol style="list-style-type: none"> (a) Bridge construction work was carried out at Bridge D and there was no discharge due to nature of works. (b) Wastewater treatment facilities were properly provided for Bridge D and function properly. (<i>Figure 1</i>) (c) As water quality mitigation measures, open slopes were covered with tarpaulin sheet or hard paved as far as practicable to minimize muddy runoff. (<i>Photos 5 & 6</i>) 6. In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to

	<p>minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. It is considered that the exceedances on 3 September 2018 were related to the impact of rainstorm and not caused by the works under the Project.</p> <p>7. According to the Event and Action Plan, the frequency of water monitoring is increase to daily. There were turbidity and SS exceedances recorded on 4 and 5 September 2018 and another investigation will be provided. Nevertheless, the Contractor should continue implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.</p>
--	---

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature : 

Date : 26 September 2018

Photo Record



Photo 1

On 3 September 2018, muddy water was observed in WM2A(a).



Photo 2

On 3 September 2018, the water quality at WM2A-C was clear.



Photo 3

During water sampling on 1 September 2018, inflow of muddy water was observed from upstream of WM2A-C that affecting the water quality of the river course.



Photo 4

On 3 September 2018, it was observed that muddy water from upstream was trapped at Nylon Dam and flowing to downstream slowly.



Photo 5

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Photo 6

As water quality mitigation measures, open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Figure 1 Location Map for Water Quality Monitoring Locations WM2A(a), WM2A-Control and work area under Contract 6

Agreement No. CE 45/2008

Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works

Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008	
Date		5 September 2018	7 September 2018
Location		WM2A(a)	
Time		11:10	10:40
Parameter		Suspended solids (mg/L)	
Action Level		14.6 AND 120% of upstream control station of the same day	
Limit Level		17.3 AND 130% of upstream control station of the same day	
Measured Levels	WM2A-C	5.0	<2
	WM2A(a)	16.0	19.0
Exceedance		Action Level	Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided by the Contractor of Contract 6 (CCKJV), construction activities carried out on 5 and 7 September 2018 at Bridge D (upstream of WM2A(a)) were mainly bridge construction. The monitoring locations and work boundary are shown in <i>Figure 1</i>. 2. According to the site photo taken by the monitoring team on 5 and 7 September 2018, the water observed in WM2A(a) was slightly turbid while the water quality at WM2A-C was clear. It was noted that some turbid water was generated when passing the loose soil at river edge. (<i>Photos 1 to 4</i>) 3. Inspection on the wastewater treatment facility SH-18 was carried out by CCKJV on 5 and 7 September 2018 upon exceedances recorded. It was observed that wastewater treatment facility SH-18 was function properly and effluent was generally in good condition. (<i>Photos 5 & 6</i>) As advised by CCKJV, wastewater treatment facilities SH-15 and SH-16 were not in operation and only stand-by on site. 4. Weekly joint site inspections among the RE, IEC, CCKJV and ET were conducted on 6 September 2018 at Bridge D to audit the site environmental performance and implementation of mitigation measures, the observation during the site inspection is summarized below. <ol style="list-style-type: none"> (a) Bridge construction work was carried out at Bridge D and there was no discharge due to nature of works. (b) Wastewater treatment facilities were properly provided for Bridge D and function properly. (<i>Figure 1</i>) (c) As water quality mitigation measures, open slopes were covered with tarpaulin sheet or hard paved as far as practicable to minimize muddy runoff. (<i>Photos 7 & 8</i>) 5. In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. In view 	

	<p>of the river water was affected by the loose soil at the river edge, it is considered that the exceedances on 5 and 7 September 2018 were not likely caused by the works under the Project.</p> <p>6. According to the Event and Action Plan, the frequency of water monitoring shall be increased to daily when exceedance recorded. The necessity of additional monitoring is relying on the turbidity result since it is in-suit measurement. There were no additional monitoring conducted on 6 and 8 September 2018 as no turbidity exceedance recorded at previous day. Moreover, there were no turbidity and SS exceedances recorded at subsequent monitoring on 11 and 13 September 2018. Nevertheless, the Contractor should continue implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.</p>
--	---

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature :



Date : 8 October 2018

Photo Record



Photo 1

On 5 September 2018, the water quality observed in WM2A(a) was slightly turbid. It was noted turbid water was generated when passing the loose soil at river edge.



Photo 2

On 5 September 2018, the water quality at WM2A-C was clear.



Photo 3

On 7 September 2018, the water quality observed in WM2A(a) was slightly turbid. It was noted turbid water was generated when passing the loose soil at river edge.



Photo 4

On 7 September 2018, the water quality at WM2A-C was clear.



Photo 5

Inspection on the wastewater treatment facility SH-18 was carried out on 5 September 2018 and it was observed that SH-18 was function properly and effluent was generally in good condition.



Photo 6

Inspection on the wastewater treatment facility SH-18 was carried out on 7 September 2018 and it was observed that SH-18 was function properly and effluent was generally in good condition.



Photo 7

Open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Photo 8

Open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Figure 1 Location Map for Water Quality Monitoring Locations WM2A(a), WM2A-Control and work area under Contract 6

Agreement No. CE 45/2008

Liantang/ Heung Yuen Wai Boundary Control Point and Associated Works

Investigation Report on Action or Limit Level Non-compliance

Project		CE 45/2008	
Date		18 September 2018	
Location		WM2A(a)	
Time		10:05	
Parameter		Turbidity (NTU)	Suspended solids (mg/L)
Action Level		24.9 AND 120% of upstream control station of the same day	14.6 AND 120% of upstream control station of the same day
Limit Level		33.8 AND 130% of upstream control station of the same day	17.3 AND 130% of upstream control station of the same day
Measured Levels	WM2A-C	9.9	<2
	WM2A(a)	33.5	27.5
Exceedance		Action Level	Limit Level
Investigation Results, Recommendations & Mitigation Measures		<ol style="list-style-type: none"> 1. According to the site information provided by the Contractor of Contract 6 (CCKJV), construction activity carried out on 18 September 2018 at Bridge D (upstream of WM2A(a)) was mainly bridge construction. The monitoring locations and work boundary are shown in <i>Figure 1</i>. 2. According to the site photo taken by the monitoring team on 18 September 2018, the water observed in WM2A(a) was slightly turbid while the water quality at WM2A-C was clear. (<i>Photos 1 to 2</i>) 3. According to the weather information from the Observatory, Typhoon Mangkhut attacked Hong Kong during 14 to 17 September and brought rainfall of 167.5mm and 12.0mm on 16 and 17 September 2018 respectively. The water quality of the water course of highly affected by the stirred up sediment and runoff from the surrounding environmental even outside the site area. During water quality monitoring on 18 September 2018, deflation of Nylon Dam was observed and the muddy water was generated when rapid flow stirred up sediment. (<i>Photo 3</i>) 4. Weekly joint site inspections among the RE, IEC, CCKJV and ET was conducted on 20 September 2018 at Bridge D to audit the site environmental performance and implementation of mitigation measures, the observation during the site inspection is summarized below. <ol style="list-style-type: none"> (a) Bridge construction work was carried out at Bridge D and there was no discharge due to nature of works. (b) Water quality at river course adjacent to site area was visually clear. (<i>Photo 4</i>) (c) Wastewater treatment facility SH-18 functioned properly and effluent was generally in good condition. (<i>Photo 5</i>) (d) As water quality mitigation measures, open slopes were covered with tarpaulin sheet or hard paved as far as practicable to minimize muddy 	

	<p>runoff. (<i>Photos 6 & 7</i>)</p> <p>5. In our investigation, CCKJV had implemented water quality mitigation measures such as providing tarpaulin sheet for open slope and surface to minimize muddy runoff. There was no adverse water quality impact observed during the site inspection at works area of Bridge D. In view of the river water was affected stirred up sediment during deflation of Nylon Dam, it is considered that the exceedances on 18 September 2018 were not likely caused by the works under the Project.</p> <p>6. According to the Event and Action Plan, the frequency of water monitoring shall be increased to daily when exceedance recorded. There were no turbidity and SS exceedances recorded at subsequent monitoring on 19 and 20 September 2018. Nevertheless, the Contractor should continue implement the water mitigation measures as recommended in the implementation schedule for environmental mitigation measures in the EM&A Manual.</p>
--	--

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature :



Date : 9 October 2018

Photo Record



Photo 1

On 18 September 2018, the water quality observed in WM2A(a) was slightly turbid. It was noted turbid water was generated when passing the loose soil at river edge.



Photo 2

On 18 September 2018, the water quality at WM2A-C was clear.



Photo 3

During water quality monitoring on 18 September 2018, deflation of Nylon Dam was observed and the muddy water was generated when rapid flow stirred up sediment.



Photo 4

During site inspection on 20 September 2018, it was observed that the water quality at river course adjacent to site area was visually clear.



Photo 5

During site inspection on 20 September 2018, it was observed that wastewater treatment facility SH-18 functioned properly and effluent was generally in good condition.



Photo 7

Open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Photo 7

Open slopes were covered with tarpaulin sheet as far as practicable to minimize muddy runoff.



Figure 1 Location Map for Water Quality Monitoring Locations WM2A(a), WM2A-Control and work area under Contract 6

Appendix O

Investigation Report for Complaint

(Not Used)
