

MTR Corporation Limited

Sheung Shui to Lok Ma Chau Spur Line

Monthly EM&A Report for Kwu Tung Station

(January 2024)

Verified by:



Adi Lee
Independent Environmental Checker
Meinhardt Infrastructure and Environment
Limited
2859 5443

Date:

16 February 2024


MTR Corporation Limited

Sheung Shui to Lok Ma Chau Spur Line

Monthly EM&A Report for Kwu Tung Station

(January 2024)

Certified by:



Viola Tong
Environmental Team Leader
MTR Corporation Limited
2621 7298

Date:




16 Feb 2024

MTR Corporation Limited

Contract 1601

Kwu Tung Station on East Rail Line

Monthly EM&A Report (January 2024) (Version 3.0)

	Name	Post	Signature	Date
Prepared by:	Jack Chow	Environmental Team Member		16 February 2024
Checked by:	Tandy Tse	Senior Environmental Consultant		16 February 2024
Certified by:	F. C. Tsang	Environmental Team Leader		16 February 2024

Contents

EXECUTIVE SUMMARY	1
Introduction.....	1
Breaches of Action and Limit Levels	1
1 PROJECT INFORMATION	3
1.1 Background	3
2 AIR QUALITY MONITORING	6
2.1 Monitoring Requirement	6
2.2 Monitoring Location.....	6
2.3 Monitoring Equipment.....	6
2.4 Monitoring Parameters, Frequency and Duration.....	7
2.5 Monitoring Methodology and QA/QC Procedure	7
2.6 Maintenance/Calibration.....	7
2.7 Environmental Quality Performance Limits	8
2.8 Results and Observations	8
2.9 Event and Action Plan	9
3 NOISE MONITORING	10
3.1 Monitoring Requirements.....	10
3.2 Monitoring Location.....	10
3.3 Monitoring Equipment.....	10
3.4 Monitoring Parameters, Frequency and Duration.....	11
3.5 Monitoring Methodology and QA/QC Procedures	11
3.6 Maintenance and Calibration	11
3.7 Results and Observations	12
3.8 Event and Action Plan	12
4 LANDSCAPE AND VISUAL MONITORING	13
4.1 Monitoring Requirements.....	13
5 ENVIRONMENTAL SITE INSPECTION	14
5.1 Site Audits	14
5.2 Implementation Status of Environmental Mitigation Measures	15
5.3 Solid and Liquid Waste Management Status	15
6 ENVIRONMENTAL NON-COMFORMANCE	16
6.1 Summary of Exceedances	16
6.2 Summary of Environmental Non-Compliance	16
6.3 Summary of Environmental Complaint	16
6.4 Summary of Environmental Summons and Successful Prosecution	16
7 FUTURE KEY ISSUES	17
7.1 Construction Programme for the upcoming reporting month	17
7.2 Potential Environmental Impacts and Recommended Mitigation Measure in the Coming Month(s).....	17
7.3 Monitoring Schedule for the Next Month	17
7.4 Construction Programme for the Next Month	17
8 CONCLUSION AND RECOMMENDATIONS	16
8.1 Conclusions.....	16

8.2 Recommendations..... 16

Appendices

Appendix A	Construction Programme
Appendix B	Calibration Certificates of Monitoring Equipment
Appendix C	Environmental Monitoring Schedules
Appendix D	Air Quality Monitoring Results and Graphic Presentation
Appendix E	Noise Monitoring Results and Graphic Presentation
Appendix F	Weather Condition
Appendix G	Event and Action Plan
Appendix H	Summary of Exceedance
Appendix I	Environmental Mitigation Implementation Schedule (EMIS)
Appendix J	Waste Flow Table for Reporting Month
Appendix K	Cumulative statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions
Appendix L	Complaint Log
Appendix M	Observation and Rectification Photos

Figures

Figures 1	Project Location
Figures 2	Air and Noise Monitoring Locations
Figures 2a	Location of representative Air and Noise Sensitive Receivers
Figures 3	Organization Structure

Tables

Table 1.1	Relevant Environmental Licenses, Permits and/or Notifications
Table 1.2	Summary of Status of Required Submission of FEP under FEP-06/129/2002/I
Table 2.1	Location for Air Quality Monitoring Locations
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.4	Action and Limit Levels for 1-hour TSP
Table 2.5	Summary of 1 – hour TSP Monitoring Results
Table 2.6	Observation at Air Quality Monitoring Stations
Table 3.1	Action and Limit Levels for Construction Noise
Table 3.2	Location of Noise Monitoring Stations
Table 3.3	Noise Monitoring Equipment
Table 3.4	Noise Quality Monitoring Parameters, Frequency and Duration
Table 3.5	Summary of Noise Monitoring Results during in the Reporting Month
Table 3.6	Observation at Noise Monitoring Station
Table 5.1	Observations and Recommendations of Site Audit
Table 7.1	Summary Table for Site Activities, Potential Environmental Impacts and Recommended Mitigation Measure in the Coming Months

EXECUTIVE SUMMARY

Introduction

Construction of Kwu Tung Station on East Rail Line [KTU(EAL)] (hereinafter referred to as "the Project") has commenced since February 2023.

Works Contract 1633 - Alteration and Addition Works at Kwu Tung for East Rail Line Protection Works" was awarded to Kum Shing (K.F.) Construction Company Limited to carry out the alteration and additional works to the existing railway facilities within the Project Site in order to facilitate the future construction of the Project. Wellab Limited was appointed by Kum Shing as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the Works Contract 1633 from 20 February 2023 to 31 October 2023 in view of the completion of alteration and additional works in October 2023.

Works Contract 1601 - Kwu Tung Station on East Rail Line was awarded to Dragages Hong Kong Limited in September 2023 to carry out the main civil works for the Project. Aurecon Hong Kong Limited was commissioned by Dragages Hong Kong Limited as the ET to provide EM&A services and take over the EM&A programme of the Project from 1 November 2023 to ensure that the environmental performance of the Works Contractor complies with the requirements specified in the Environmental Permit (EP no. FEP-06/129/2002/I), Environmental Review Report (ERR) and Updated EM&A Manual under this EP for the Kwu Tung Station on the East Rail Line and other relevant statutory requirements. The weekly environmental site inspections and environmental monitoring as scheduled under EM&A programme was conducted by Aurecon with effect from 1 November 2023.

This is the 3rd Monthly Environmental Monitoring and Audit (EM&A) Report for the Works Contract 1601 - Kwu Tung Station on East Rail Line (hereinafter called the "Works Contract") under Environmental Permit No. FEP-06/129/2002/I. This report was prepared by Aurecon Hong Kong Ltd. (Aurecon) which summaries findings of the EM&A programme during the reporting period from 1 January 2024 to 31 January 2024.

Breaches of Action and Limit Levels

Air Quality

1. No Action and Limit Level exceedance was recorded for air quality monitoring in the reporting month.

Construction Noise

2. No Action and Limit Level exceedance was recorded for construction noise monitoring in the reporting month.

Environmental Non-Compliance

3. No environmental non-compliance was recorded in the reporting month.

Complaint log

4. No complaint was received in the reporting period.

Notification of Summons and Successful Prosecutions

5. No notifications of summons and successful prosecutions were received in the reporting period.

Reporting Changes

6. There were no reporting changes in the reporting month.

Future Key Issues

7. The main works will be anticipated in the next three months are as follow:

Upper Platform and KTU Site (Above-ground); Station Tunnel Box (Under-ground):

- Site installation (Above-ground Works)
- Haul road formation (Above-ground Works)
- Hoarding erection & site office erection (Above-ground Works)
- Flood wall erection (Above-ground Works)
- Mucking out (Above-ground Works)
- Alteration and Additional works inside the tunnel (Under-ground Works)
- Station excavation work (Above-ground Works)

9. Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality, waste management and landscape and visual impact issues.

1 PROJECT INFORMATION

1.1 Background

- 1.1.1 The Environmental Impact Assessment (EIA) report for “Sheung Shui to Lok Ma Chau Spur Line” (Register No.: AEIAR-052/2002) (hereafter called the “approved EIA”) conducted by Kowloon-Canton Railway Corporation (KCRC) was approved in 2002, and addressed the environmental impacts caused by the LMC Spur Line. As far as the railway station at Kwu Tung is concerned, the approved EIA had considered the potential construction and operational impacts for the railway station at Kwu Tung enabling works including the station box structure.
- 1.1.2 In December 2020, the MTR Corporation Limited (i.e., MTRCL, hereafter called the Project Proponent) was invited by the Government to commence the detail planning and design of the railway station at Kwu Tung.
- 1.1.3 The construction and operation of the LMC Spur Line constitutes to Item A.2 Designated Project (DP) “A railway and its associated stations”, under Part I Schedule 2 of Environmental Impact Assessment Ordinance (EIAO). KCRC had applied for and had been granted numbers of Environmental Permits (EPs) and Further Environmental Permits (FEP) for its construction and operation of LMC Spur Line, including the existing tunnel box and enabling works.
- 1.1.4 In order to expand the scope of the FEP (No. FEP-06/129/2002/H) held by MTRCL to cover the construction and operation of the proposed Kwu Tung Station on the East Rail Line (hereinafter called “the Project”), variation of this FEP was required. The Environmental Review Report (ERR) had been prepared and submitted under the VEP application. The VEP application had been approved and a new Environmental Permit (No. FEP- 06/129/2002/I) was granted by EPD on 24 December 2021.
- 1.1.5 Construction of Kwu Tung Station on East Rail Line [KTU(EAL)] has commenced since February 2023.
- 1.1.6 Works Contract 1633 - Alteration and Addition Works at Kwu Tung for East Rail Line Protection Works” was awarded to Kum Shing (K.F.) Construction Company Limited to carry out the alteration and additional works to the existing railway facilities within the Project Site in order to facilitate the future construction of the Project. Wellab Limited was appointed by Kum Shing as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the Works Contract 1633 from 20 February 2023 to 31 October 2023 in view of the completion of alteration and additional works in October 2023.
- 1.1.7 Works Contract 1601 - Kwu Tung Station on East Rail Line was awarded to Dragages Hong Kong Limited in September 2023 to carry out the main civil works for the Project. Aurecon Hong Kong Limited was commissioned by Dragages Hong Kong Limited as the ET to provide EM&A services and take over the EM&A programme of the Project from 1 November 2023 to ensure that the environmental performance of the Works Contractor complies with the requirements specified in the Environmental Permit (EP no. FEP-06/129/2002/I), Environmental Review Report (ERR) and Updated EM&A Manual under this EP for the Kwu Tung Station on the East Rail Line and other relevant statutory requirements. The weekly environmental site inspections and environmental monitoring as scheduled under EM&A programme was conducted by Aurecon with effect from 1 November 2023.
- 1.1.8 This is the 3rd monthly Environmental Monitoring and Audit (EM&A) Report for Contract 1601 Kwu Tung Station on East Rail Line under Environmental Permit No. FEP-06/129/2002/I. This report was prepared by Aurecon Hong Kong Ltd. (Aurecon) presenting the EM&A works carried out during the reporting period from 1 to 31 January 2024.
- 1.1.9 The scope of works under the Kwu Tung Station on the East Rail Line comprises the following:
- Excavation of the fill material above the existing tunnel box;

- Modification of existing tunnel box structures;
- Construction of concourse and platform areas;
- Construction of back-of-house areas;
- Construction of entrances, Ventilation Buildings (VB) and Fire Rescue Stairs (FRS);
- Modification of existing Emergency Access Point (EAP)/ Emergency Egress Point (EEP);
- Relocation of existing EVA and associated facilities; and
- Construction of other station associated facilities and underground adit.

1.1.10 The construction area of the Project is shown in **Figure 1**.

Project Organization

1.1.11 The project organization and contact details are shown in **Figure 3**.

Summary of Construction Works Undertaken During Reporting Month

1.1.12 The major site activities undertaken in the reporting month included:

Upper Platform and KTU Site (Above-ground); Station Tunnel Box (Under-ground Works):

- Site installation (Above-ground Works)
- Haul road formation (Above-ground Works)
- Hoarding erection & site office erection (Above-ground Works)
- Concrete paving (Above-ground Works)
- Flood wall erection (Above-ground Works)
- Alteration and Additional works inside the tunnel (Under-ground Works)

Construction Programme

1.1.13 Construction Programme from the Contractor is given in **Appendix A**.

Status of Environmental Licenses, Notifications and Permits

1.1.14 A summary of the status of the relevant permits, licenses and/or notifications on environmental protection for this project is presented in **Table 1.1**.

Table 1.1 Relevant Environmental Licenses, Permits and/or Notifications

Environmental License / Permit / Notification	Reference Number	Valid From	Valid Till	Status
Environmental Permit for whole project	FEP-06/129/2002/I	24/12/2021	N/A	Valid
Notification pursuant to Air Pollution Control (Construction Dust) Regulation	Ref No.: 497363	22/09/2023	N/A	Valid
Billing Account for Disposal of Construction Waste	Account No.: 7048687	16/10/2023	N/A	Valid
Registration of Chemical Waste Producer	5213-545-D2939-01	08/12/2023	N/A	Valid
Effluent Discharge License under	500018	TBA	N/A	Submitted on 23/11/2023;

Water Pollution Control Ordinance				Application pending.
Construction Noise Permit (CNP)	GW-RN0049-24	19/01/2024	08/03/2024	Valid

Submission Status under the Environmental Permits

1.1.15 The status of required submission under Environmental Permit (EP) conditions under FEP-06/129/2002/I are summarized in **Table 1.2**.

Table 1.2 Summary of Status of Required Submission for FEP-06/129/2002/I

EP Conditions (FEP-06/129/2002/I)	Submission	Submission Date
1.11	Notification of Commencement Date of Construction of the Project	19 January 2022
2.8	Updated Environmental Monitoring and Audit (EM&A) Manual (Oct 2022)	28 September 2022 (1st submission) 25 October 2022 (2nd submission) 7 November 2022 (Approved)
2.9	Management Organizations	18 January 2023 (1st submission) 1 November 2023 (2nd submission)
2.10	Project Layout Plan of Kwu Tung Station	11 November 2022 15 November 2022 (Deposited)
2.11	Landscape and Visual Plan	6 February 2023 (1st submission) 15 September 2023 (2nd submission) 18 September 2023 (Deposited)
4.3	Baseline Monitoring Report (Dec 2022)	9 December 2022
4.4	Monthly EM&A Report (December 2023)	15 January 2024

2 AIR QUALITY MONITORING

2.1 Monitoring Requirement

- 2.1.1 According to the Updated EM&A Manual of the Project, 1 - hour Total Suspended Particulates shall be conducted at least 3 times every six days. A sampling frequency shall be strictly observed at all the monitoring stations.
- 2.1.2 Since November 2023, Aurecon Hong Kong Limited (Aurecon) has taken over the role of ET from Wellab Limited to carry out the air quality impact monitoring.

2.2 Monitoring Location

- 2.2.1 According to Section 5.5.7 of the Updated EM&A Manual, five air quality monitoring locations, namely CD1a, CD2a, CD3a, CD4a, CD5 are covered under the Project as shown in **Figure 2**. The locations of the representative air sensitive receivers (ASR) around the Project as identified in the ERR are shown in **Figure 2a**. **Table 2.1** describes the location of the air quality monitoring stations.

Table 2.1 Location for Air Quality Monitoring Locations

Monitoring Station ID	Description
CD1a	Village Houses along Ma Tso Lung Road
CD2a	Village Houses near Shek Tsai Leng
CD3a	Village Houses along Ho Sheung Heung Road
CD4a	Construction site office of Advance Site Formation and Engineering Infrastructure Works at Kwu Tung North and Fanling North New Development Areas – Contract No. ND/2019/01
CD5	Multi-Welfare Services Complex

Remark: Since Kwu Tung North Multi-Welfare Services Complex has been in service, air quality monitoring location of Dills Corner Garden (CD5a) was relocated back to this Complex (CD5) to carry out monitoring since December 2023, in accordance with the Section 5.5.7 of the approved Updated EM&A Manual of the Project.

2.3 Monitoring Equipment

- 2.3.1 Upon approval of the IEC, 1-hour TSP levels can be measured by direct reading method with using handheld dust meter, which is capable of producing comparable results as that by the high-volume sampling method, to indicate short event impacts.
- 2.3.2 The proposed use of handheld dust meter was submitted to the IEC and agreement was obtained from the IEC in accordance with Section 5.4.5 of the Updated EM&A Manual.
- 2.3.3 **Table 2.2** summarizes the equipment used in the air quality monitoring programme. Copies of calibration certificates are attached in **Appendix B**.

Table 2.2 Air Quality Monitoring Equipment

Equipment	Model	Serial Number
Portable Dust Meter – 1- hour TSP	SIBATA Digital Dust Indicator (Model: LD-5R)	0Z4545
		851816
		882106
		882150

		942532
--	--	--------

2.3.4 In accordance with Section 5.6.3 and 5.6.4 of the Updated EM&A Manual, Meteorological information extracted from “Hong Kong Observatory - Ta Kwu Ling Weather Station” is used as the alternative method to obtain representative wind data. For Ta Kwu Ling Weather Station, it is located nearby the Project site and situated at approximately 15m above mean sea level. The station’s wind data monitoring equipment is set above the existing ground 10 meters in compliance with the general setting up requirements. Furthermore, this station also provides other meteorological information, such as humidity, rainfall, air pressure and temperature etc.

2.4 Monitoring Parameters, Frequency and Duration

2.4.1 The parameters, duration and frequency for air quality impact monitoring is given in **Table 2.3**. Monitoring stations CD1a, CD2a, CD3a, CD4a and CD5 were set up in accordance to the requirements for placement of equipment, as set out in Section 5.5.7 of the Updated EM&A manual of the Project.

Table 2.3 Air Quality Monitoring Parameters, Frequency and Duration

Parameters	Frequency
1 – hour TSP	3 times for every 6 days

2.5 Monitoring Methodology and QA/QC Procedure

1-hour TSP Air Quality Monitoring

Instrumentation

2.5.1 The measuring procedures of the handheld dust meter are in accordance with the Manufacturer’s Instruction Manual as follows:

2.5.2 Handheld dust meter was deployed for the air quality monitoring location as shown in **Table 2.1**.

2.5.3 The measuring procedures and equipment set-up of the 1-hour dust meters were in accordance with the Manufacturer’s Instruction Manual as follow:

- Securely fix the meter at a level of 0.9m to 1.9m from ground, at a position with unrestricted airflow around the meter.
- Pull up the air sampling inlet cover.
- Change the Mode 0 to BG with once.
- Push Start/Stop switch once.
- Turn the knob to SENSI.ADJ and press it.
- Push Start/Stop switch once.
- Return the knob to the position MEASURE slowly.
- Push the timer set switch to set measuring time.
- Remove the cap and make a measurement.

2.6 Maintenance/Calibration

2.6.1 The following maintenance/calibration was required for the direct dust meters:

- Check and calibrate the dust meter by high volume sampler (HVS) to check the validity and accuracy of the results measured by direct reading method. Calibration of dust meter should be carried out every six months throughout all stages of the air quality monitoring. The calibration certificates of the monitoring equipment are presented in **Appendix B**.
- The correlation coefficient was checked to establish the correlation relationship between the handheld dust meter and HVS. The correlation factor was determined by comparing the results of HVS and handheld dust meter.

- Checking is made prior to air quality monitoring commencing to ensure all equipment is in good working condition with necessary power supply. Zero count test were conducted before and after each monitoring event.
- The calibration of environmental equipment used was cross checked by the IEC to confirm the precision of the application.

2.7 Environmental Quality Performance Limits

2.7.1 The baseline monitoring results formed the basis for determining the air quality criteria for the impact monitoring. The ET shall compare the impact monitoring results with air quality criteria set up for 1-hour TSP. Based on the baseline dust monitoring data and the derivation criteria specified above, the summary of baseline air quality monitoring results and Action/Limit Levels are presented in **Table 2.4**.

Table 2.4 Action and Limit Levels for 1-hour TSP

Monitoring Location	Range of Baseline Monitoring Results ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
CD1a	15 - 90	275	500
CD2a	14 - 104	279	
CD3a	17 - 122	279	
CD4a	19 - 173	281	
CD5	19 - 172	280	

2.8 Results and Observations

2.8.1 The Impact air quality monitoring result are summarized in **Table 2.5**. Detailed monitoring results and graphical presentations of air quality monitoring results are shown in **Appendix D**.

Table 2.5 Summary of 1 - hour TSP Monitoring Results

Monitoring Location	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level, ($\mu\text{g}/\text{m}^3$)
CD1a	56	30 - 101	275	500
CD2a	55	33 - 93	279	
CD3a	44	29 - 56	279	
CD4a	61	37 - 109	281	
CD5	62	39 - 113	280	

2.8.2 The schedule of air quality monitoring in the reporting month is shown in **Appendix C**.

2.8.3 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedances was recorded.

2.8.4 According to our field observations, the major dust sources identified at the designated air quality monitoring stations in the reporting month are shown in **Table 2.6**:

Table 2.6 Observation at Air Quality Monitoring Stations

Monitoring Station	Major Dust Sources
CD1a	No sources of dust emission was observed.
CD2a	No sources of dust emission was observed.
CD3a	No sources of dust emission was observed.
CD4a	1. Other construction site: Vehicle emission 2. Road traffic
CD5	1. Project construction site: Excavation, drilling rig, generator, dump truck, excavator breaker, mobile crane truck, cement truck 2. Other construction site: Vehicle emission

2.8.5 The weather information during the reporting period is summarized in **Appendix F**.

2.9 Event and Action Plan

2.9.1 Should non-compliance of the air quality criteria occur, actions in accordance with the Action Plan in **Appendix G** shall be carried out.

3 NOISE MONITORING

3.1 Monitoring Requirements

- 3.1.1 In accordance with the Updated EM&A Manual, construction noise monitoring shall be conducted in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}) to monitor the construction noise arising from the construction activities.
- 3.1.2 The regular monitoring frequency for each monitoring station was on a weekly basis and one set of measurements between 0700 and 1900 hours on normal weekdays shall be conducted. **Table 3.1** shows the established Action and Limit Levels for the environmental monitoring works.

Table 3.1 Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A)

3.2 Monitoring Location

- 3.2.1 According to Section 6.5.4 of the Updated EM&A Manual, one designated noise monitoring station for the Project is shown in **Figure 2**. The location of the representative noise sensitive receivers (NSR) around the Project as identified in the ERR are shown in **Figure 2a**. **Table 3.2** describes the location of the noise monitoring station.

Table 3.2 Location of Noise Monitoring Station

Monitoring Station(s)	Location(s)
CN1	Multi-Welfare Services Complex

Remark: Since Kwu Tung North Multi-Welfare Services Complex has been in service, noise monitoring location of Dills Corner Garden (CN1a) was relocated back to this Complex (CN1) to carry out monitoring since December 2023, in accordance with the Section 6.5.4 of the approved Updated EM&A Manual of the Project.

3.3 Monitoring Equipment

- 3.3.1 As referred to the requirements of the Technical Memorandum (TM) issued under the NCO, the sound level meters in compliance with the International Electro technical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications should be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement, the accuracy of the sound level meter should be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The measurements may be accepted as valid only if the difference between calibration levels obtained before and after the noise measurement is less than 1.0 dB (94 dB \pm 0.1 dB).
- 3.3.2 **Table 3.3** summarizes the noise monitoring equipment used. Copies of calibration certificates are attached in **Appendix B**.

Table 3.3 Noise Monitoring Equipment

Equipment	Manufacturer	Model	Serial Number
Sound Level Meter	NTi Audio	XL2	A2A-09696-E0
Acoustical Calibrator	RION	NC-75	34724245

3.4 Monitoring Parameters, Frequency and Duration

3.4.1 The parameters and frequencies of impact noise monitoring is summarized in **Table 3.4**. Monitoring stations CN1 was set up in accordance with the requirements for placement of equipment, as set out in Section 6.5.4 of the Updated EM&A manual of the Project.

Table 3.4 Noise Quality Monitoring Parameters, Frequency and Duration

Parameters and duration	Frequency	Measurement
30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays. L_{eq} , L_{10} and L_{90} would be recorded.	Once per week	Façade

3.5 Monitoring Methodology and QA/QC Procedures

3.5.1 Noise measurement should be conducted as the following procedures:

- The sound level meter was set on a tripod at a point 1m from the exterior of the noise sensitive façade and at the position of 1.2m above the ground;
- For free field measurement, the meter was positioned away from any nearby reflective surfaces. Free field noise levels were adjusted with a correction of +3 dB(A);
- The battery condition was checked to ensure good functioning of the meter;
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - frequency weight: A
 - time weighting: Fast
 - measurement time: L_{eq} (30-mins) dB(A)
(As six consecutive L_{eq} (5-mins) during non-restricted hours (i.e., 0700-1900 hrs. on normal weekdays))
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re- calibration or repair of the equipment;
- During the monitoring period, the L_{eq} , L_{90} and L_{10} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet;
- Noise measurement was paused temporarily during periods of high intrusive noise (e.g., dog barking, helicopter noise) if possible and observation record during measurement period should be provided; and
- Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s. The wind speed should be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.6 Maintenance and Calibration

3.6.1 Maintenance and calibration procedures should also be carried out, including:

- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory.
- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- Immediately prior to and following each noise measurement, the accuracy of the sound level meter should be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements would be accepted as valid only if the calibration levels before and after the noise measurement agreed to within 1.0 dB.

- The calibration of environmental equipment used was cross checked by the IEC to confirm the precision of the application.

3.7 Results and Observations

3.7.1 The noise monitoring results are summarized in **Table 3.5**. Detailed monitoring results and graphical presentations of noise monitoring are shown in **Appendix E**.

Table 3.5 Summary of Noise Monitoring Results during in the Reporting Month

Monitoring Station	Time Period	Noise Level Leq (30-mins) dB(A)	Limit Level dB(A)
CN1	Daytime (0700 – 1900)	69.6 – 73.7	75

3.7.2 The schedule of noise monitoring in reporting month is shown in **Appendix C**.

3.7.3 Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. The summary of exceedance record in reporting month is shown in **Appendix H**.

3.7.4 According to our field observations, the major noise sources identified at the designated noise monitoring station in the reporting month are shown in **Table 3.6**:

Table 3.6 Observation at Noise Monitoring Station

Monitoring Station	Major Noise Source
CN1	<ol style="list-style-type: none"> 1. Construction noise from project site: Excavation, drilling rig, generator, dump truck, excavator breaker, mobile crane truck, cement truck 2. Other construction site: Generator, cement truck, excavation, crane, crane truck and dump truck 3. Road traffic

3.7.5 The weather information for noise monitoring during reporting period is summarized in **Appendix F**.

3.8 Event and Action Plan

3.8.1 Should non-compliance of the noise monitoring criteria occur, actions in accordance with the Event and Action Plan in **Appendix G** shall be carried out.

4 LANDSCAPE AND VISUAL MONITORING

4.1 Monitoring Requirements

- 4.1.1 In accordance with Section 11.3 of the Updated EM&A Manual, site audit should be undertaken during the construction phase of the Project to check that the proposed landscape and visual mitigation measures are properly implemented and maintained as per their intended objectives.
- 4.1.2 Site inspections of the implementation of landscape and visual mitigation measures were conducted by ET at least once per month during the construction period. The observation and recommendations made during the audit sessions are summarized in **Table 5.1**. The implementation status is given in **Appendix I**.

5 ENVIRONMENTAL SITE INSPECTION

5.1 Site Audits

5.1.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out on 03, 10, 17, 24 and 31 January 2024. The site inspection held on 17 January 2024 was a joint inspection with the MTR's Representative, IEC, the Contractor, and the ET during the reporting period.

5.1.2 No non-conformance was identified during the site inspections in the reporting month. Key observations during the site inspections in the reporting period are summarized in **Table 5.1**. The observation and rectification photos are attached in **Appendix M**.

Table 5.1 Observations and Recommendations of Site Audit

Date	Environmental Observation(s) / Recommendation(s)	Follow-up Status	Close-out Date / Status
2024 - 1 - 03	No Major environmental issue was observed during the site inspection.	NA	NA
2024 - 1 - 10	No Major environmental issue was observed during the site inspection.	NA	NA
2024 - 1 - 17	Observation: 1. Haul Road should be sprayed water to enhance dust mitigation measure. (Upper platform) 2. Stockpile should be covered by tarpaulin sheet. (Upper platform)	Action Taken: 1. Haul road was sprayed water to control dust. (Upper platform) 2. Stockpile was removed. (Upper platform)	Rectified on 17 January 2024.
2024 - 1 - 24	No Major environmental issue was observed during the site inspection.	NA	NA
2024 - 1 - 31	No Major environmental issue was observed during the site inspection.	NA	NA

5.2 Implementation Status of Environmental Mitigation Measures

- 5.2.1 In accordance with the Updated EM&A Manual, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix I**.

5.3 Solid and Liquid Waste Management Status

- 5.3.1 In accordance with the Updated EM&A Manual, waste management was audited during weekly site audit to ensure that the recommended good practices and other measures recommended in the EMIS of the Updated EM&A Manual (provided in **Appendix I**) are properly implemented by the Contractor. Waste management practice including waste handling, storage, transportation, and disposal were audited.
- 5.3.2 The Contractor is advised to minimize the wastes generated through recycling or reusing. All mitigation measures stipulated in the Updated EM&A Manual shall be properly implemented. The status of implementation of waste management and reduction measures are summarized in **Appendix I**.
- 5.3.3 Waste generated from this Project includes inert C&D materials and non-inert C&D materials. Non inert C&D materials are made up of general refuse and waste that cannot be reused or recycled and have to be disposed of at the designated landfill sites. The amount of wastes generated by the construction works of the Project during the reporting month is shown in **Appendix J**.

6 ENVIRONMENTAL NON-COMFORMANCE

6.1 Summary of Exceedances

6.1.1 No exceedance of Action or Limit Levels of air quality was recorded in the reporting period.

6.1.2 No exceedance of Action or Limit Levels of construction noise was recorded in the reporting period.

6.2 Summary of Environmental Non-Compliance

6.2.1 No environmental non-compliance was recorded in the reporting period.

6.3 Summary of Environmental Complaint

6.3.1 There was no environmental complaint received in the reporting month. The Cumulative Complaint Log since the commencement of the Project is presented in **Appendix L**.

6.4 Summary of Environmental Summons and Successful Prosecution

6.4.1 There was no successful environmental prosecution or notification of summons received since the Project commencement. The Cumulative Log for environmental summon and successful prosecution since the commencement of the Project is presented in **Appendix K**.

7 FUTURE KEY ISSUES

7.1 Construction Programme for the upcoming reporting month

7.1.1 Major activities in the upcoming month:

Upper Platform and KTU Site (Above-ground); Station Tunnel Box (Under-ground):

- Site installation (Above-ground Works)
- Haul road formation (Above-ground Works)
- Hoarding erection & site office erection (Above-ground Works)
- Flood wall erection (Above-ground Works)
- Alteration and Additional works inside the tunnel (Under-ground Works)
- Station excavation work (Above-ground Works)
- Mucking out (Above-ground Works)

7.2 Potential Environmental Impacts and Recommended Mitigation Measure in the Coming Month(s)

7.2.1 With reference to the site layout plan including the indication of coming three months construction site activities in **Appendix A**, potential environmental impacts arising from the above construction activities are mainly associated with construction dust, noise, water quality, waste management, landscape and visual. The foreseeable environmental impacts were taken into consideration of the planned mitigation measures in the coming months.

7.2.2 The major site activities, potential environmental and recommended mitigation measures for the coming three months are shown in **Table 7.1**.

7.3 Monitoring Schedule for the Next Month

7.3.1 The tentative environmental monitoring schedule for the next month is shown in **Appendix C**.

7.4 Construction Programme for the Next Month

7.4.1 A tentative construction programme is provided in **Appendix A**.

Table 7.1 Summary Table for Site Activities, Potential Environmental Impacts and Recommended Mitigation Measure in the Coming Months

Contract No.	Major Site Activities	Location	Potential Environmental Impact	Recommended Mitigation Measures
1601	I. Site installation	KTU site and Upper platform (Above-ground)	<ul style="list-style-type: none"> ➤ Construction Dust impact ➤ Noise Impact (Construction Phase) ➤ Water Quality Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	<p><u>Air Quality</u></p> <ul style="list-style-type: none"> ▪ Watering on exposed earth and dry haul road. ▪ Cover the stockpiles or dusty materials when not in use. ▪ Provide shelter with top and 3-sides for cement production activities. ▪ Any excavation or earthmoving operation shall spray with water immediately before, during and immediately after the operation so as to maintain the entire surface wet. ▪ Close the mechanical cover of the vehicles used for transporting dusty materials. ▪ Wheel washing was provided for every vehicle before leaving site. ▪ Conduct air quality monitoring regularly. <p><u>Construction Noise</u></p> <ul style="list-style-type: none"> ▪ Mobile plant should be sited as far away from NSRs as possible and practicable. ▪ Quieter plant should be chosen as far as practicable. ▪ Vehicles and plants used on-site were checked regularly to ensure that vehicles and plants were operating normally. ▪ Vehicles were turned off when not in use. ▪ Conduct noise monitoring regularly. ▪ Provide temporary noise screens if necessary. ▪ Obtain Construction Noise Permit (CNP) for works to be carried out
	II. Haul road formation		<ul style="list-style-type: none"> ➤ Construction Dust impact ➤ Noise Impact (Construction Phase) ➤ Water Quality Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	
	III. Hoarding erection & site office erection		<ul style="list-style-type: none"> ➤ Construction Dust impact ➤ Noise Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	

	IV. Flood wall erection		<ul style="list-style-type: none"> ➤ Noise Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	<p>during restricted hours and follow the conditions stipulated in the CNP issued by the Noise Control Authority.</p> <p><u>Water Quality</u></p> <ul style="list-style-type: none"> ▪ Set up wastewater treatment system (AquaSed) on site. <p><u>Waste / Chemical Management</u></p>
	V. Mucking out		<ul style="list-style-type: none"> ➤ Construction Dust impact ➤ Noise Impact (Construction Phase) ➤ Water Quality Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	<ul style="list-style-type: none"> ▪ Stockpiling area should be provided with covers and water spraying system to prevent materials from windblown or being washed away. ▪ Chemical cabinet available on site. ▪ Recycling bins, general bins and storage area should provide. ▪ Provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling.
	VI. Station excavation work		<ul style="list-style-type: none"> ➤ Construction Dust impact ➤ Noise Impact (Construction Phase) ➤ Water Quality Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	
	VII. Alteration and Additional works inside the tunnel	Station Tunnel Box (Under-ground)	<ul style="list-style-type: none"> ➤ Noise Impact (Construction Phase) ➤ Waste Management (Construction Waste) 	

8 CONCLUSION AND RECOMMENDATIONS

8.1 Conclusions

- 8.1.1 This report summarized the Monitoring Results and Audits findings of the EM&A Programme Under the EP of the Project during the reporting period from 1 January to 31 January 2024.
- 8.1.2 1-hour TSP impact monitoring was carried out in the reporting month. No Action or Limit Level exceedance at CD1a, CD2a, CD3a, CD4a and CD5 was recorded during the period.
- 8.1.3 Day time construction noise monitoring was carried out in the reporting month. No Action or Limit Level exceedance at CN1 was recorded during the period.
- 8.1.4 Environmental site inspections were carried out on 03, 10, 17, 24 and 31 January 2024.
- 8.1.5 No environmental non-compliance was recorded in the reporting month.
- 8.1.6 No environmental complaint, notification of summons and successful prosecution was recorded in the reporting month.

8.2 Recommendations

- 8.2.1 According to the environmental audits performed in the reporting month, the following recommendation was made:

Air Quality

During dry and windy season, the Contractors are reminded to pay special attention on the air quality mitigation measures such as watering of dry haul roads and exposed earth, loose soil construction surface, and covering of dusty materials with impervious sheet should be implemented as far as practicable.







Water Quality




Water quality mitigation measures as recommended in the EM&A Manual should be fully implemented. The Contractor is reminded not to make any discharge before a discharge licence is granted.

Construction Noise



Construction noise would be a key environmental issue during construction phase of the project. Noise mitigation measures such as using quieter plants and installation of temporary noise barriers at the construction noise predominate area should be implemented in accordance with the EM&A requirement.

Figures 1 Project Location

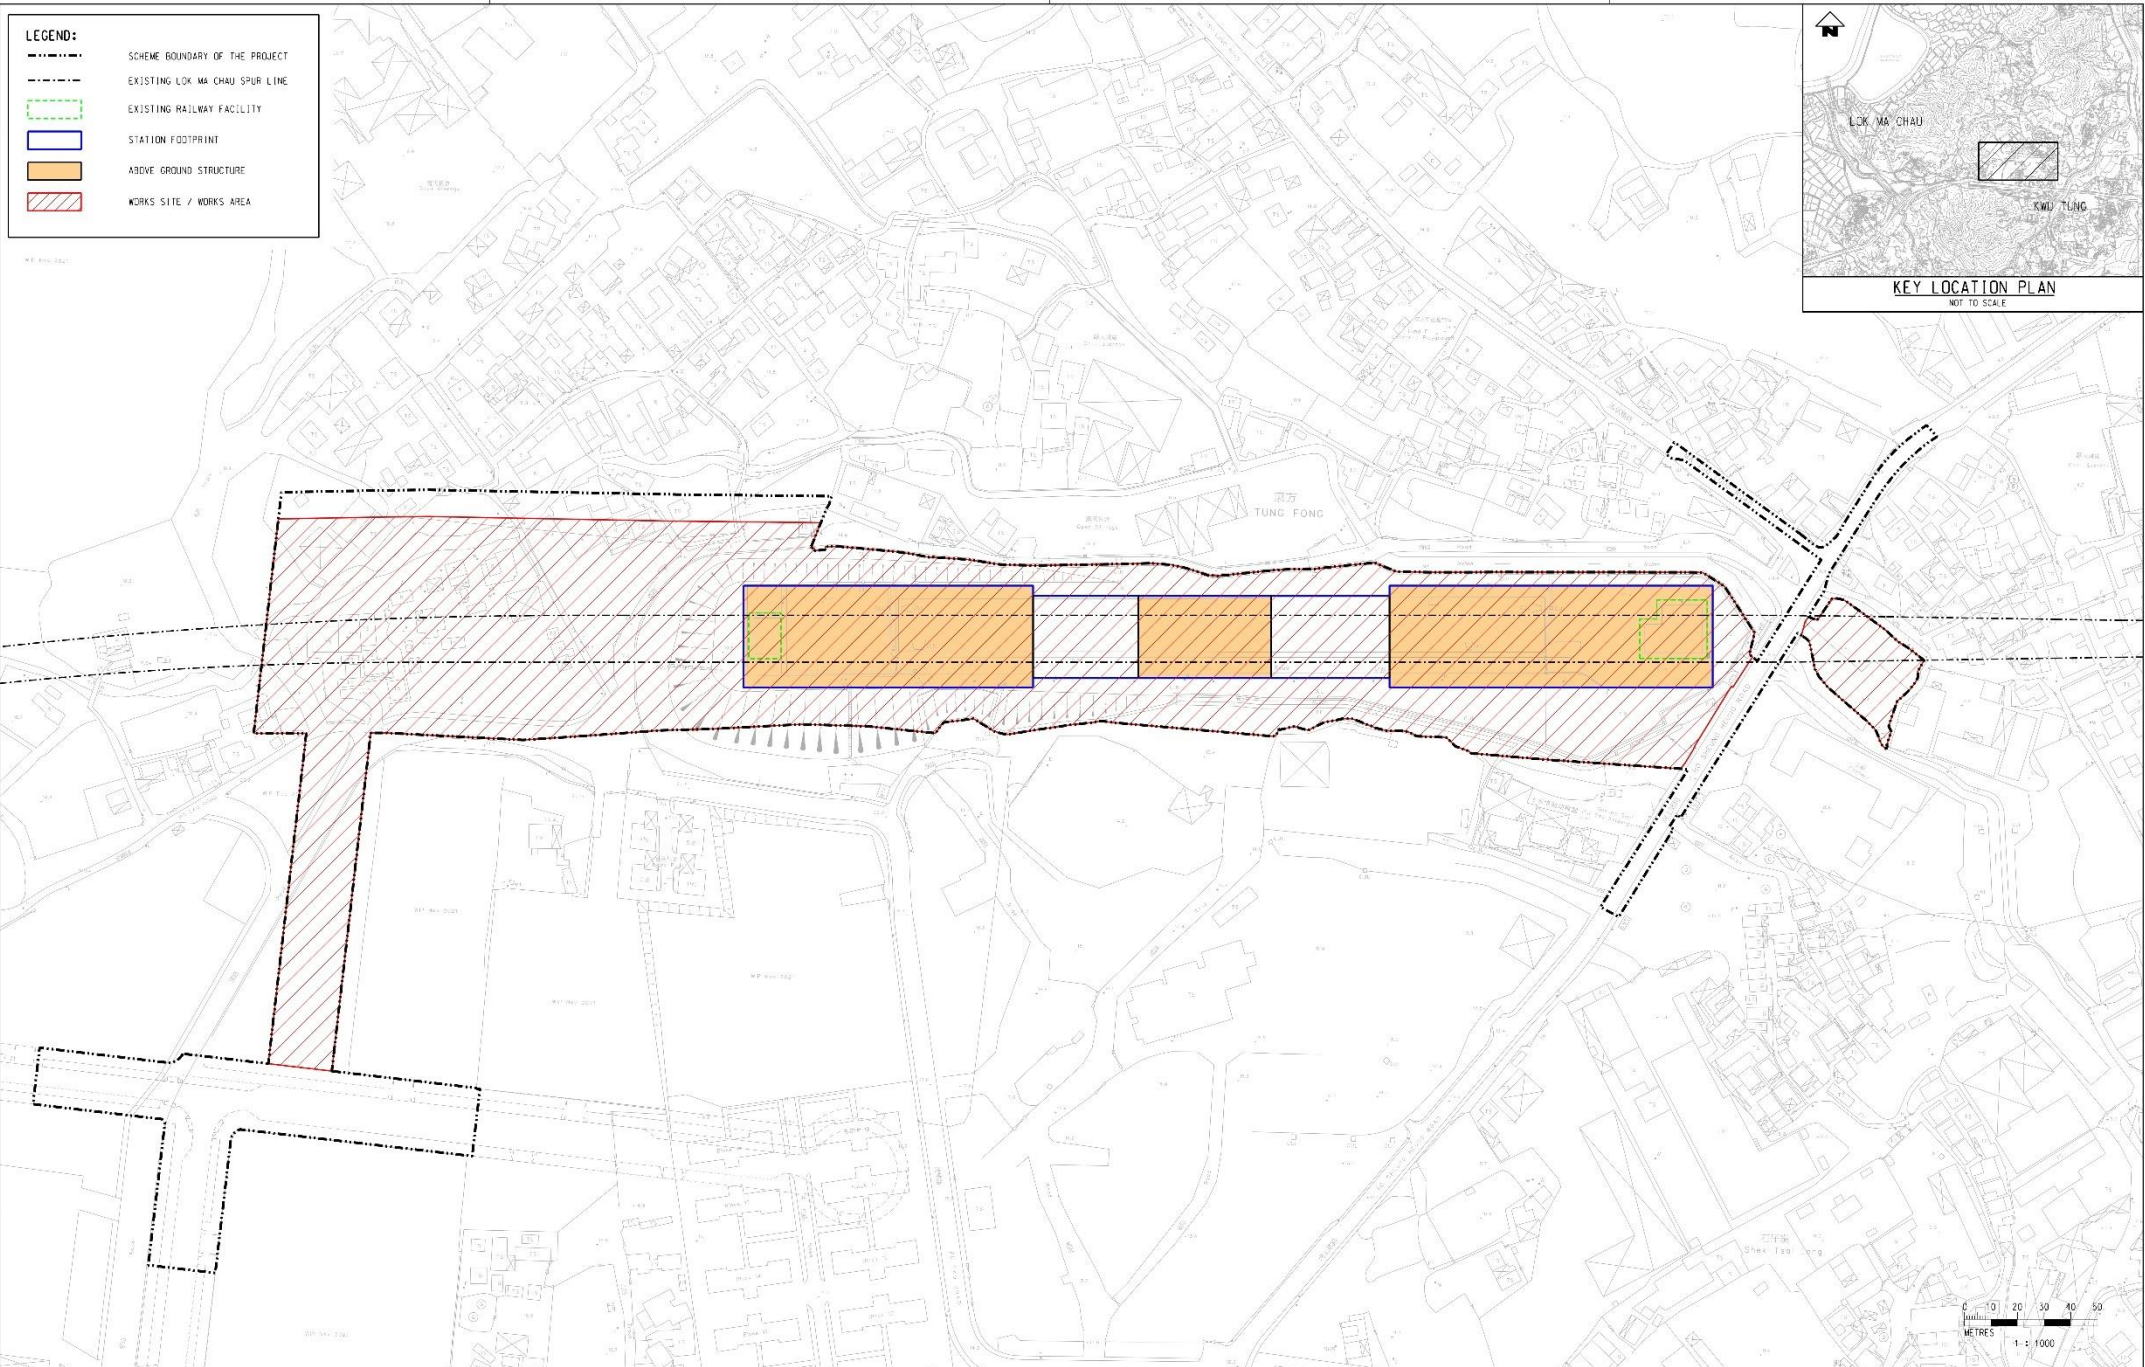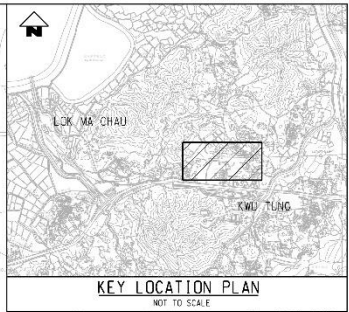- LEGEND:**
-  SCHEME BOUNDARY OF THE PROJECT
 -  EXISTING LOK MA CHAU SPUR LINE
 -  EXISTING RAILWAY FACILITY
 -  STATION FOOTPRINT
 -  ABOVE GROUND STRUCTURE
 -  WORKS SITE / WORKS AREA



18/10/2022 10:43:43 AM
 18/10/2022 10:43:43 AM
 18/10/2022 10:43:43 AM


DRAWN: WM		 Supported by:  ARCADIS	TITLE
DESIGNED: KP			RAILWAY STATION AT KWU TUNG
CHECKED: HKS			PROJECT LAYOUT PLAN
APPROVED: CYH			Figure 1
DATE	18/OCT/2022	ORIGINATOR	SCALE
SUBMISSION OF PROJECT LAYOUT PLAN 18/OCT/2022		CADD REF: C1601-B-KTU-OAP-A11-051A.dgn	DRAWING NO: C1601/B/KTU/OAP/A11/051
BY	DATE	APPROVED	REV.
			A

Figures 2 Air and Noise Monitoring Locations

Figures 2a Location of representative Air and Noise Sensitive Receivers

Figure 3 Organization Structure

MTR

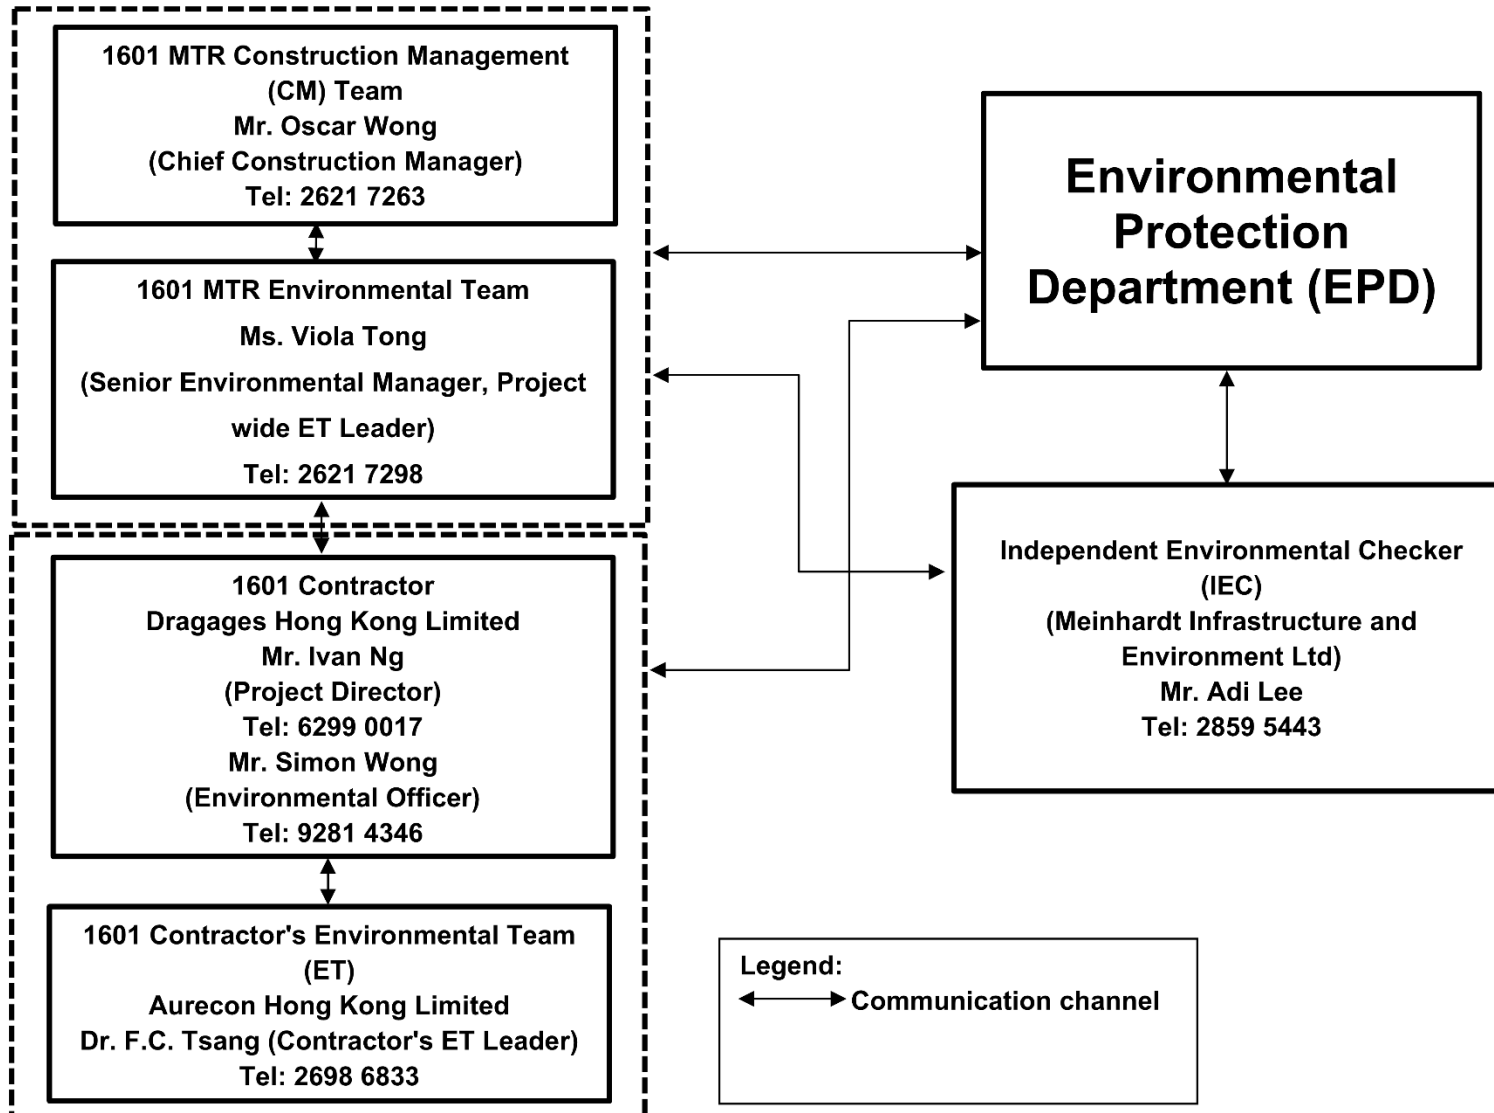

Legend:
 ← → Communication channel

Title

Contract 1601 – Kwu Tung Station on East Rail Line
 Project Organisation for Environmental Works



Appendix A Construction Programme

3-Month Rolling Programme for Major Works (Tentative)

Item	Activity Description	2024			
		Jan	Feb	Mar	Apr
1	KTU Station				
	Site Office Erection				
	Site Installation				
	Hoarding Erection				
	Haul Road Formation				
	Flood Wall Erection				
	Station Excavation Work				
	Mucking Out Activity				
2	Existing Facility Modification (Platform & Track Level)				
	Modification of Demontable Wall				
	Civil Works Provision for PSD Installation				
	Evacuation Walkway Diversion & Hoarding Works				

Appendix B Calibration Certificates of Monitoring Equipment

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipment

Verification Test Date:	28-Nov-23	to	30-Nov-23	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	0Z4545				
Our Report Reference No.:	RPT-23-HVS-0065				
Calibration Location:	AM2, location near the Leachate Treatment Works within the NENTX Landfill				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24


Equipment Verification Result


Verification Test No.	Date	Duration			Results from Calibrated Equipment		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration ($\mu\text{g}/\text{m}^3$) y-axis
1	28/11/2023	8789.68	8792.68	180.00	15648	87	96
2	28/11/2023	8792.68	8795.68	180.00	14993	83	85
3	28/11/2023	8795.68	8798.68	180.00	8635	48	49
4	30/11/2023	8798.68	8801.68	180.00	10501	58	67
5	30/11/2023	8801.68	8804.68	180.00	24622	137	145
6	30/11/2023	8804.68	8807.68	180.00	9145	51	56

Linear Regression of y on x

Slope, K factor:	1.0451	Intercept:	2.1545	*Correlation Coefficient, R:	0.9957
Verification Test Result:	Strong Correlation, Results were accepted.			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

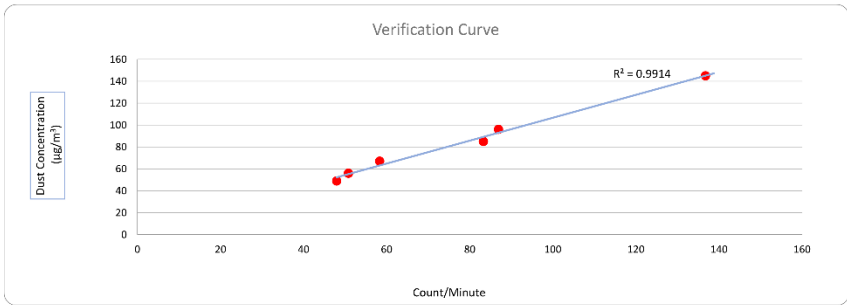

Operated By: Andy Li  Date: 30-11-2023
 Project Technician, Environmental

Checked By: Tandy Tse  Date: 30-11-2023
 Senior Consultant, Environmental

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement

Verification Test Date:	28-Nov-23	to	30-Nov-23	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	851816				
Our Report Reference No.:	RPT-23-HVS-0067				
Calibration Location:	AM2, location near the Leachate Treatment Works within the NENTX Landfill				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24

Equipment Verification Result


Verification Test No.	Date	Duration			Results from Calibrated Equipement		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration ($\mu\text{g}/\text{m}^3$) y-axis
1	28/11/2023	8789.68	8792.68	180.00	16023	89	96
2	28/11/2023	8792.68	8795.68	180.00	15213	85	85
3	28/11/2023	8795.68	8798.68	180.00	8823	49	49
4	30/11/2023	8798.68	8801.68	180.00	10698	59	67
5	30/11/2023	8801.68	8804.68	180.00	24980	139	145
6	30/11/2023	8804.68	8807.68	180.00	9653	54	56

Linear Regression of y on x

Slope, K factor:	1.0418	Intercept:	0.6307	*Correlation Coefficient, R:	0.9961
Verification Test Result:	Strong Correlation, Results were accepted.			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

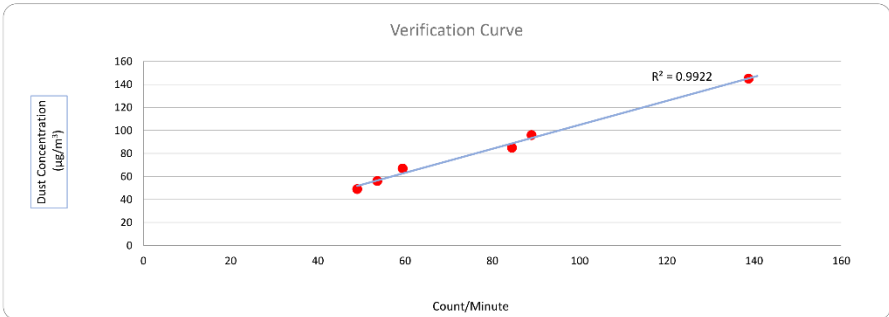

Operated By: Andy Li  Date: 30-11-2023
 Project Technician, Environmental

Checked By: Tandy Tse  Date: 30-11-2023
 Senior Consultant, Environmental

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement

Verification Test Date:	28-Nov-23	to	30-Nov-24	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	882106				
Our Report Reference No.:	RPT-23-HVS-0068				
Calibration Location:	AM2, location near the Leachate Treatment Works within the NENTX Landfill				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24

Equipment Verification Result


Verification Test No.	Date	Duration			Results from Calibrated Equipement		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration ($\mu\text{g}/\text{m}^3$) y-axis
1	28/11/2023	8789.68	8792.68	180.00	15546	86	96
2	28/11/2023	8792.68	8795.68	180.00	14944	83	85
3	28/11/2023	8795.68	8798.68	180.00	8543	47	49
4	30/11/2023	8798.68	8801.68	180.00	10499	58	67
5	30/11/2023	8801.68	8804.68	180.00	24622	137	145
6	30/11/2023	8804.68	8807.68	180.00	9145	51	56

Linear Regression of y on x

Slope, K factor:	1.0437	Intercept:	2.4993	*Correlation Coefficient,R:	0.9958
Verification Test Result:	Strong Correlation, Results were accepted.			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

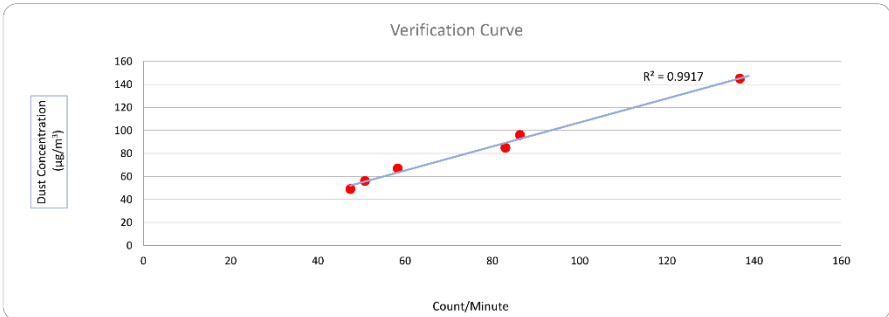

Operated By: Andy Li  Date: 30-11-2023
 Project Technician, Environmental

Checked By: Tandy Tse  Date: 30-11-2023
 Senior Consultant, Environmental

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement

Verification Test Date:	28-Nov-23	to	30-Nov-24	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	882150				
Our Report Reference No.:	RPT-23-HVS-0070				
Calibration Location:	AM2, location near the Leachate Treatment Works within the NENTX Landfill				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24

Equipment Verification Result

Verification Test No.	Date	Duration			Results from Calibrated Equipement		Results from Standard Equipment
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration ($\mu\text{g}/\text{m}^3$) y-axis
1	28/11/2023	8789.68	8792.68	180.00	15634	87	96
2	28/11/2023	8792.68	8795.68	180.00	15012	83	85
3	28/11/2023	8795.68	8798.68	180.00	8753	49	49
4	30/11/2023	8798.68	8801.68	180.00	10587	59	67
5	30/11/2023	8801.68	8804.68	180.00	25017	139	145
6	30/11/2023	8804.68	8807.68	180.00	9256	51	56

Linear Regression of y on x

Slope, K factor:	1.0289	Intercept:	2.7296	*Correlation Coefficient,R:	0.9954
Verification Test Result:	Strong Correlation, Results were accepted.			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

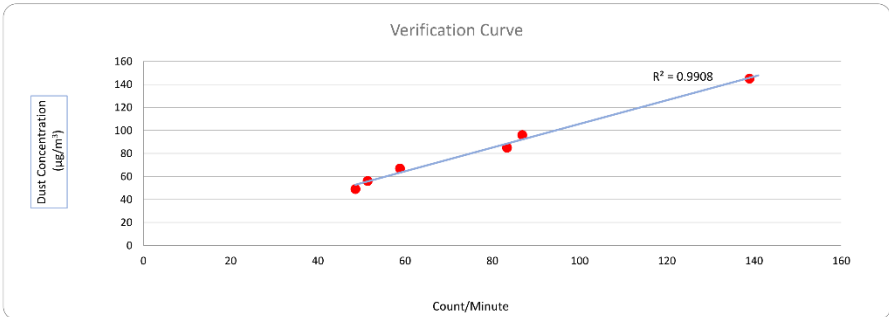

Operated By: Andy Li  Date: 30-11-2023
Project Technician, Environmental

Checked By: Tandy Tse  Date: 30-11-2023
Senior Consultant, Environmental

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement

Verification Test Date:	28-Nov-23	to	30-Nov-23	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:	Sibata LD-5R				
Unit-under-Test Serial No.:	942532				
Our Report Reference No.:	RPT-23-HVS-0071				
Calibration Location:	AM2, location near the Leachate Treatment Works within the NENTX Landfill				

Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24


Equipment Verification Result

Verification Test No.	Date	Duration			Results from Calibrated Equipement		Results from Standard Equipement
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration ($\mu\text{g}/\text{m}^3$) y-axis
1	28/11/2023	8789.68	8792.68	180.00	15446	86	96
2	28/11/2023	8792.68	8795.68	180.00	14835	82	85
3	28/11/2023	8795.68	8798.68	180.00	8320	46	49
4	30/11/2023	8798.68	8801.68	180.00	10303	57	67
5	30/11/2023	8801.68	8804.68	180.00	23517	131	145
6	30/11/2023	8804.68	8807.68	180.00	9043	50	56

Linear Regression of y on x

Slope, K factor:	1.1020	Intercept:	-0.1223	*Correlation Coefficient,R:	0.9954
Verification Test Result:	Strong Correlation, Results were accepted.			* If the Correlation Coefficient, R is <0.5. Checking and Re-verification are required.	

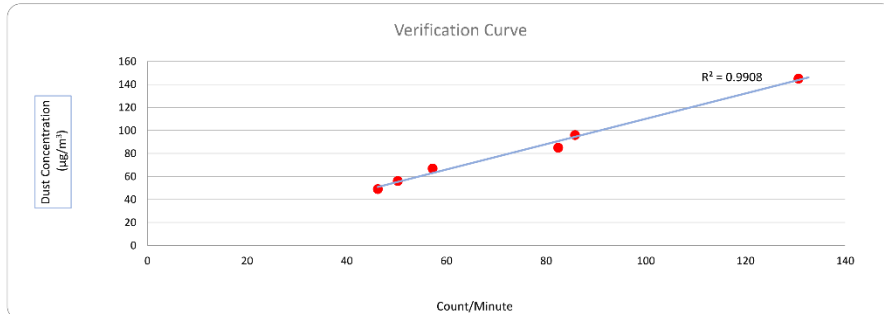

Operated By: Andy Li  Date: 30-11-2023
 Project Technician, Environmental

Checked By: Tandy Tse  Date: 30-11-2023
 Senior Consultant, Environmental



RECALIBRATION
DUE DATE:
June 19, 2024

Certificate of Calibration

Calibration Certification Information			
Cal. Date: June 19, 2023	Rootsmeter S/N: 438320	Ta: 294 °K	
Operator: Jim Tisch		Pa: 754.9 mm Hg	
Calibration Model #: TE-5025A	Calibrator S/N: 4166		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4500	3.2	2.00
2	3	4	1	1.0260	6.4	4.00
3	5	6	1	0.9170	8.0	5.00
4	7	8	1	0.8770	8.8	5.50
5	9	10	1	0.7240	12.8	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0025	0.6914	1.4190	0.9958	0.6867	0.8826
0.9983	0.9730	2.0068	0.9915	0.9664	1.2481
0.9961	1.0863	2.2436	0.9894	1.0790	1.3955
0.9951	1.1346	2.3532	0.9883	1.1270	1.4636
0.9897	1.3670	2.8380	0.9830	1.3578	1.7651
QSTD	m=	2.10188	QA	m=	1.31616
	b=	-0.03580		b=	-0.02227
	r=	0.99998		r=	0.99998

Calculations	
Vstd = $\frac{\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)}$	Va = $\frac{\Delta Vol((Pa-\Delta P)/Pa)}$
Qstd = $Vstd/\Delta Time$	Qa = $Va/\Delta Time$
For subsequent flow rate calculations:	
Qstd = $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa = $1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH:	calibrator manometer reading (in H2O)
ΔP:	rootsmeter manometer reading (mm Hg)
Ta:	actual absolute temperature (°K)
Pa:	actual barometric pressure (mm Hg)
b:	intercept
m:	slope

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
 145 South Miami Avenue
 Village of Cleves, OH 45002

www.tisch-env.com
 TOLL FREE: (877)263-7610
 FAX: (513)467-9009

Certificate of Calibration

for

Description: Sound Level Meter
Manufacturer: NTi Audio
Type No.: XL2 (Serial No.: A2A-09696-E0)
Microphone: ACO 7052 (Serial No.:68914)
Preamplifier: NTi Audio MA220 (Serial No.:10390)

Submitted by:

Customer: Acuity Sustainability Consulting Limited
Address: Unit E, 12/F, Ford Glory Plaza,
Nos. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon, Hong Kong

Upon receipt for calibration, the instrument was found to be:

- Within (31.5Hz – 4kHz)
- Outside


the allowable tolerance.


The test equipment used for calibration are traceable to National Standards via:
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 30 March 2023

Date of calibration: 04 April 2023

Date of NEXT calibration: 03 April 2024

Calibrated by: 
Calibration Technician

Certified by: 
Mr. Ng Yan Wa
Laboratory Manager

Date of issue: 04 April 2023

Certificate No.: APJ22-164-CC002



Page 1 of 4

1. Calibration Precaution:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Conditions:

Air Temperature: 21.5 °C
 Air Pressure: 1005 hPa
 Relative Humidity: 71.4 %

3. Calibration Equipment:

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV220061	HOKLAS

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.1	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.1	Ref
			104		104.1	±0.3
			114		114.1	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz		
30-130	dBA SPL	Fast	94	1000	94.1	Ref
		Slow			94.1	±0.3

Certificate No.: APJ22-164-CC002



Page 2 of 4

Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz			
30-130	dB	SPL	Fast	94	31.5	94.3	±2.0
					63	94.3	±1.5
					125	94.3	±1.5
					250	94.2	±1.4
					500	94.2	±1.4
					1000	94.1	Ref
					2000	93.8	±1.6
					4000	93.1	±1.6

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz			
30-130	dBA	SPL	Fast	94	31.5	55.0	-39.4±2.0
					63	68.2	-26.2±1.5
					125	78.2	-16.1±1.5
					250	85.6	-8.6±1.4
					500	91.0	-3.2±1.4
					1000	94.1	Ref
					2000	95.0	+1.2±1.6
					4000	94.1	+1.0±1.6

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading, dB	IEC 61672 Class 1 Specification, dB	
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz			
30-130	dBC	SPL	Fast	94	31.5	91.3	-3.0±2.0
					63	93.5	-0.8±1.5
					125	94.1	-0.2±1.5
					250	94.2	-0.0±1.4
					500	94.2	-0.0±1.4
					1000	94.1	Ref
					2000	93.6	-0.2±1.6
					4000	92.3	-0.8±1.6

Certificate No.: APJ22-164-CC002



Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong

Tel: (852) 2668 3423

Fax: (852) 2668 6946

Homepage: <http://www.aa-lab.com>E-mail: inquiry@aa-lab.com

5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.15
	63 Hz	± 0.10
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate No.: APJ22-164-CC002



Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong

Tel: (852) 2668 3423

Fax: (852) 2668 6946

Homepage: <http://www.aa-lab.com>

E-mail: inquiry@aa-lab.com

Certificate of Calibration

for

Description: Sound Level Calibrator
Manufacturer: RION
Type No.: NC-75
Serial No.: 34724245

Submitted by:

Customer: Acuity Sustainability Consulting Limited
Address: Unit E, 12/F, Ford Glory Plaza,
Nos. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon,
Hong Kong

Upon receipt for calibration, the instrument was found to be:

- Within
 Outside

the allowable tolerance.

The test equipments used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 27 July 2023

Date of calibration: 3 August 2023

Date of NEXT calibration: 2 August 2024

Calibrated by: _____
Calibration Technician

Certified by: _____
Mr. Ng Yan Wa
Laboratory Manager

Date of issue: 3 August 2023

Certificate No.: APJ23-049-CC003



Page 1 of 2

1. Calibration Precautions:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Specifications:

Calibration check

3. Calibration Conditions:

Air Temperature: 22.6 °C
Air Pressure: 1006 hPa
Relative Humidity: 52.9 %

4. Calibration Equipment:

Test Equipment	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV220061	HOKLAS
Sound Level Meter	RION NA-28	30721812	AV220120	HOKLAS

5. Calibration Results

5.1 Sound Pressure Level

Nominal value dB	Accept lower level dB	Accept upper level dB	Measured value dB
94.0	93.6	94.4	94.0

Note:

The values given in this certification only related to the values measured at the time of the calibration.

Certificate No.: APJ23-049-CC003



Page 2 of 2

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
Tel: (852) 2668 3423 Fax: (852) 2668 6946
Homepage: <http://www.aa-lab.com> E-mail: inquiry@aa-lab.com

Appendix C Environmental Monitoring Schedules

**Contract 1601 - Kwu Tung Station on East Rail Line
Impact Air Quality and Noise Monitoring Schedule**

Jan-24

Sun	Mon	Tue	Wed	Thu	Fri	Sat
1	2	3	4	5	6	7
		1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1				
7	8	9	10	11	12	13
	1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1					1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5
14	15	16	17	18	19	20
					1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1	
21	22	23	24	25	26	27
				1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1		
28	29	30	31			
			1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1			

Remarks:

1. Daytime Noise Monitoring (07:00-1900)

Note:

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Contract 1601 - Kwu Tung Station on East Rail Line
Tentative Impact Air Quality and Noise Monitoring Schedule**

Feb-24						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
				1	2	3
4	5	6	7	8	9	10
		1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1			1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5	
11	12	13	14	15	16	17
				1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1		
18	19	20	21	22	23	24
		1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1				
25	26	27	28	29		
	1-hour TSP monitoring for CD1a, CD2a, CD3a, CD4a & CD5 Daytime Noise monitoring for CN1					

Remarks:

1. Daytime Noise Monitoring (07:00-1900)

Note:

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Appendix D Air Quality Monitoring Results and Graphic Presentation

Location CD1a - Village Houses along Ma Tso Lung Road							
Date	Start Time	Weather	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2024-1-02	14:11	Sunny	95	87	88	275	500
2024-1-08	8:07	Sunny	101	96	97		
2024-1-13	8:24	Fine	41	30	31		
2024-1-19	13:08	Sunny	41	40	40		
2024-1-25	13:14	Fine	31	30	34		
2024-1-31	13:20	Sunny	44	42	35		
Average			56				
Range			30 - 101				



Location CD2a - Village Houses near Shek Tsai Leng							
Date	Start Time	Weather	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2024-1-02	8:57	Sunny	63	58	61	279	500
2024-1-08	8:00	Sunny	80	71	73		
2024-1-13	13:22	Fine	40	38	37		
2024-1-19	13:17	Sunny	39	38	44		
2024-1-25	13:33	Fine	33	33	36		
2024-1-31	9:00	Sunny	93	75	79		
Average			55				
Range			33 - 93				

Location CD3a - Village Houses along Ho Sheung Heung Road							
Date	Start Time	Weather	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2024-1-02	8:05	Sunny	56	54	55	279	500
2024-1-08	14:06	Sunny	47	46	53		
2024-1-13	8:14	Fine	40	29	29		
2024-1-19	13:57	Sunny	42	40	40		
2024-1-25	13:05	Fine	35	35	37		
2024-1-31	13:34	Sunny	56	54	44		
Average			44				
Range			29 - 56				



Location CD4a - Construction site office of Advance Site Formation and Engineering Infrastructure Works at Kwu Tung North and Fanling North New Development Areas - Contract No. ND/2019/01							
Date	Start Time	Weather	1 st Hour ($\mu\text{g}/\text{m}^3$)	2 nd Hour ($\mu\text{g}/\text{m}^3$)	3 rd Hour ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2024-1-02	8:46	Sunny	70	74	73	281	500
2024-1-08	8:23	Sunny	109	88	73		
2024-1-13	8:05	Fine	69	51	44		
2024-1-19	13:51	Sunny	46	45	44		
2024-1-25	13:47	Fine	37	41	43		
2024-1-31	13:10	Sunny	62	66	57		
Average			61				
Range			37 - 109				

Location CD5 - Multi-Welfare Services Complex							
Date	Start Time	Weather	1 st Hour (µg/m ³)	2 nd Hour (µg/m ³)	3 rd Hour (µg/m ³)	Action Level (µg/m ³)	Limit Level (µg/m ³)
2024-1-02	14:00	Sunny	70	54	68	280	500
2024-1-08	8:49	Sunny	113	99	67		
2024-1-13	8:44	Fine	62	44	39		
2024-1-19	9:01	Sunny	53	48	44		
2024-1-25	9:00	Fine	49	52	54		
2024-1-31	13:50	Sunny	66	68	71		
Average			62				
Range			39 - 113				


1-hour TSP Concentration Level

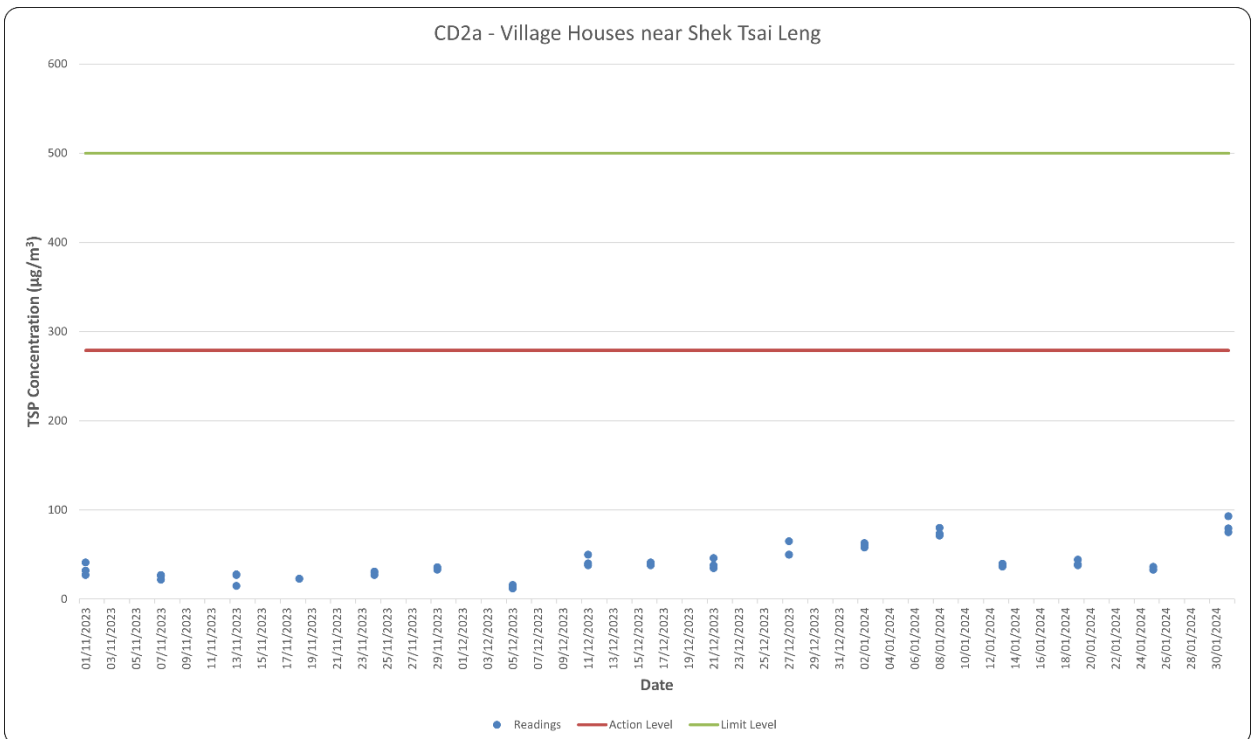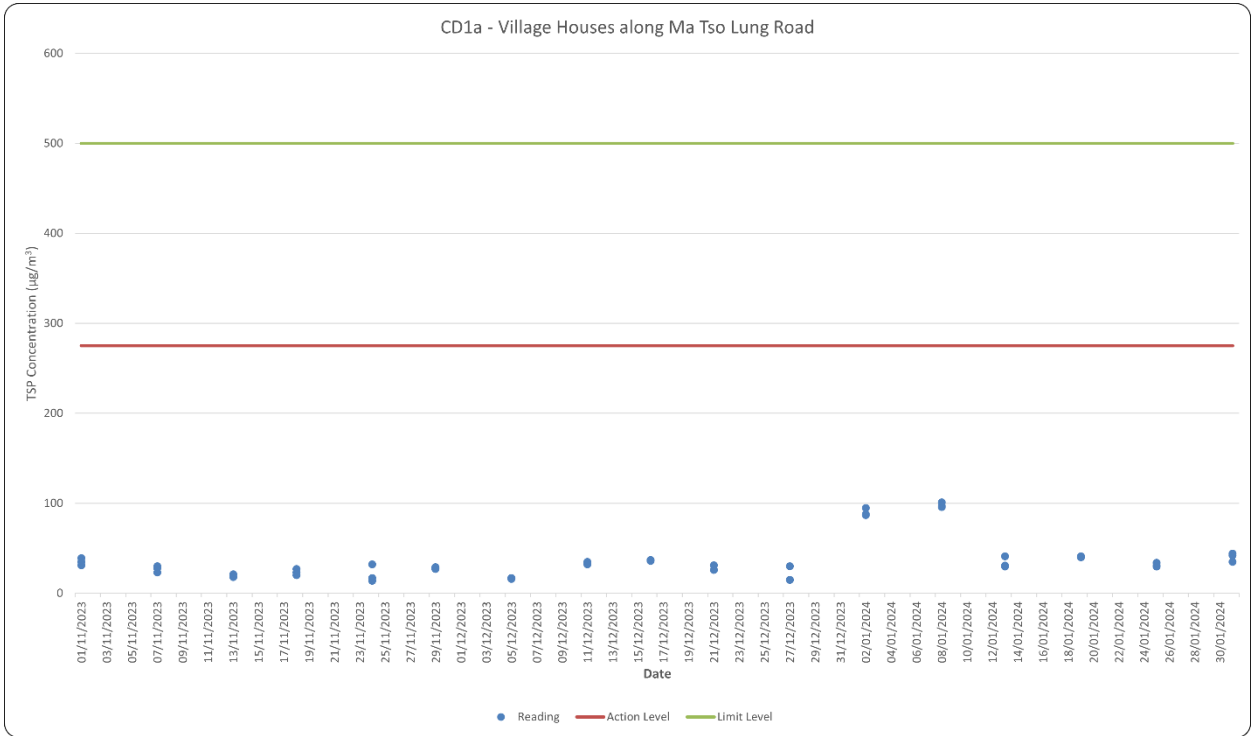

1-hour TSP Concentration Level

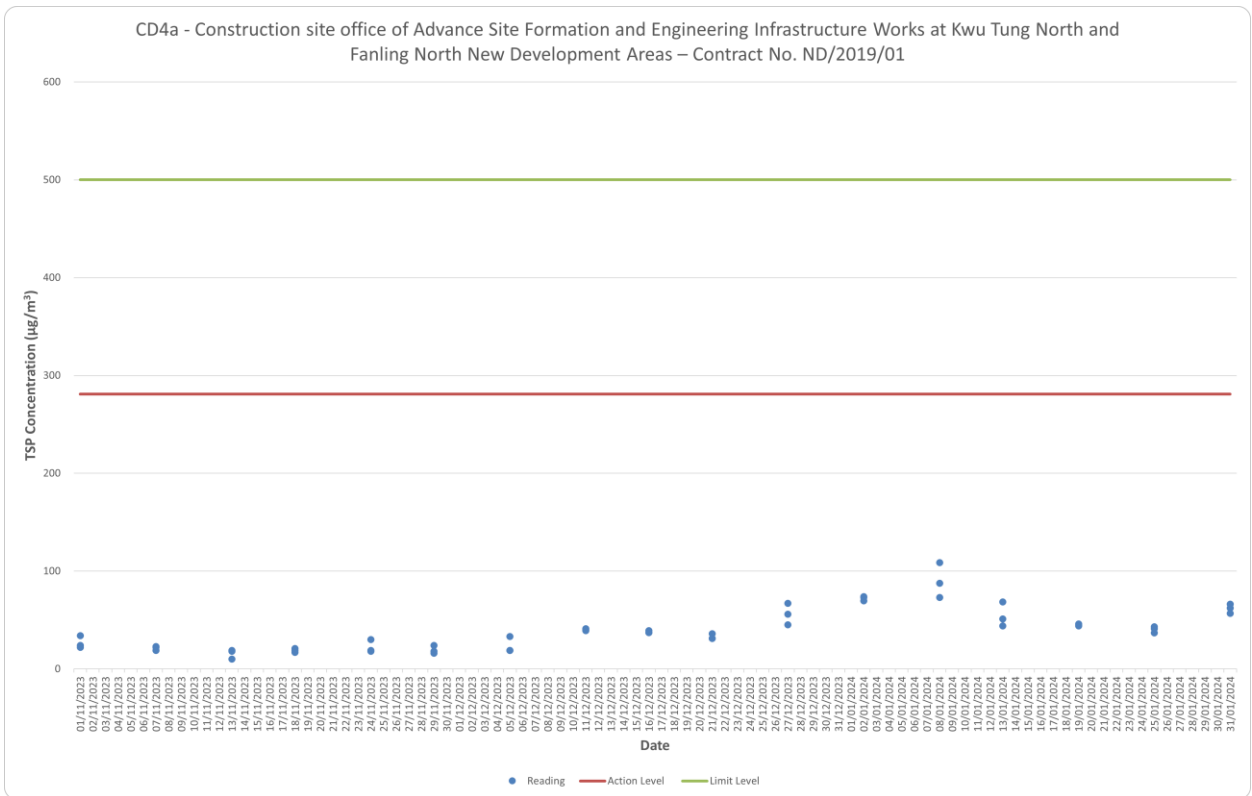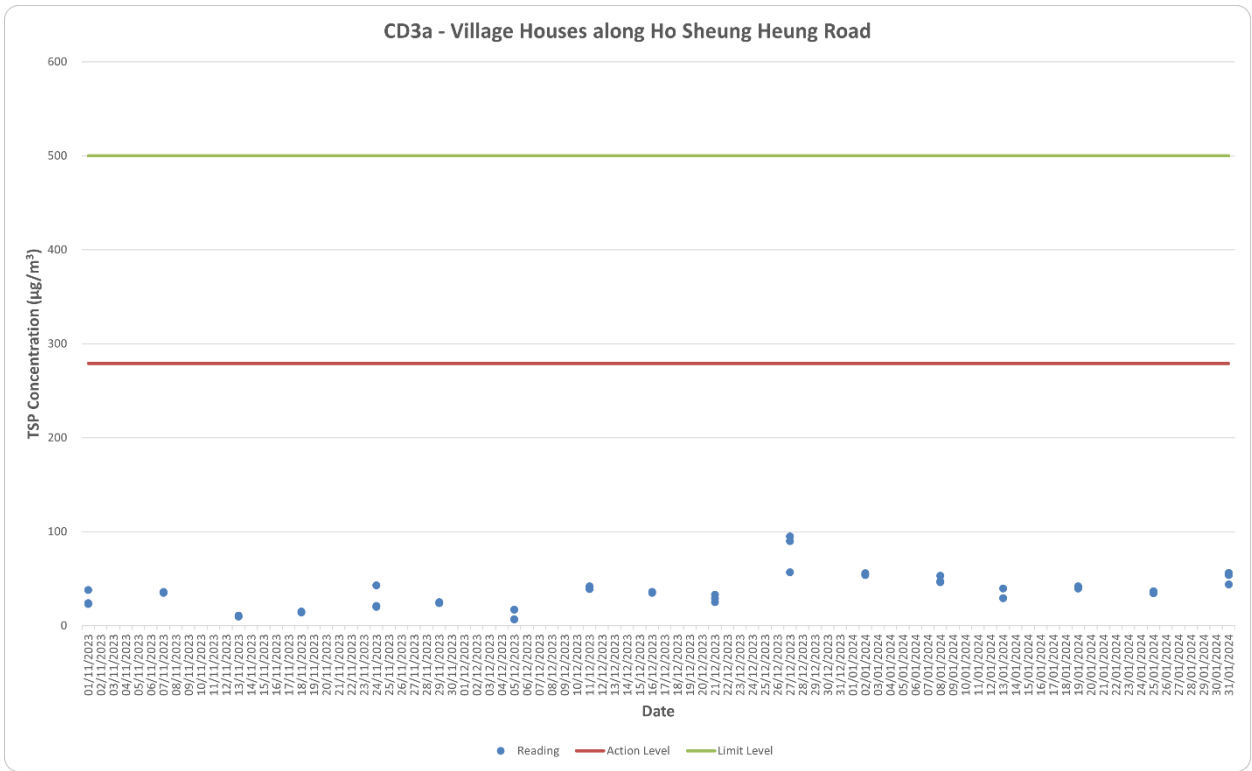

1-hour TSP Concentration Level

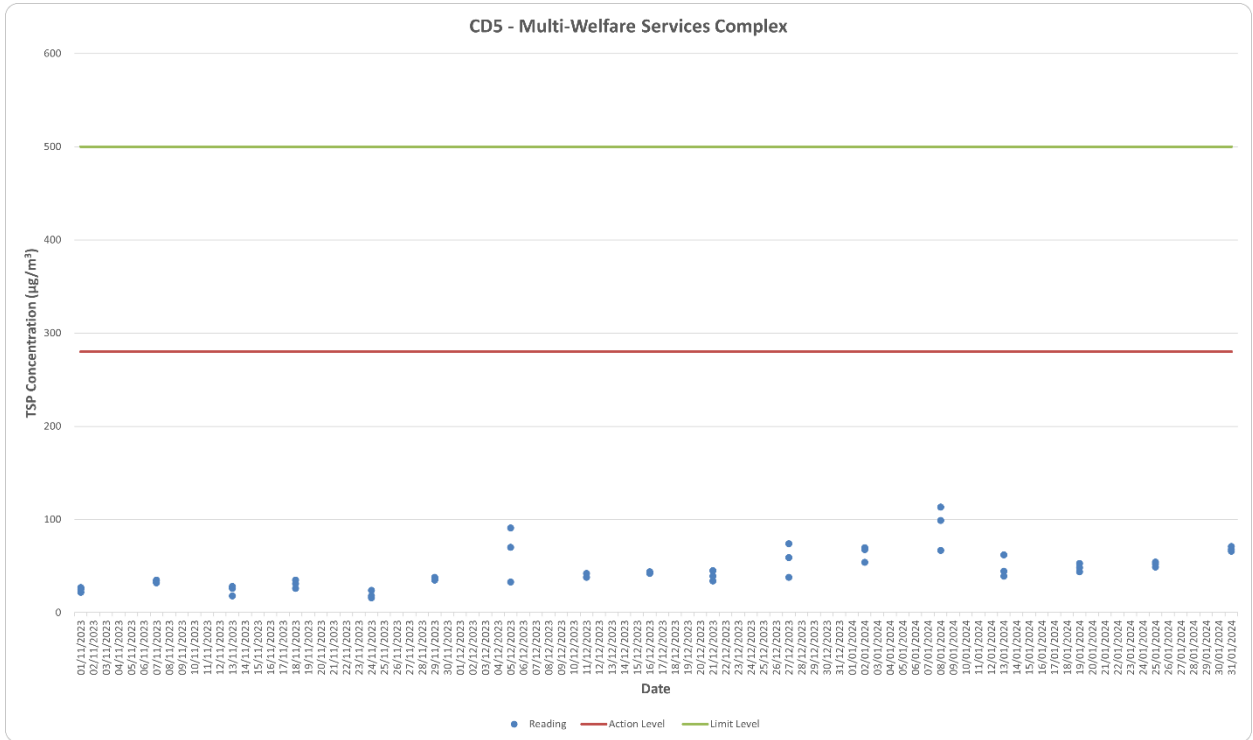


Major Construction Activities	Reporting Period		
	November 2023	December 2023	January 2024
Site clearance (Above-ground Works)	✓	✓	
Site installation (Above-ground Works)	✓	✓	✓
Haul road formation (Above-ground Works)	✓	✓	✓
Hoarding erection (Above-ground Works)	✓	✓	✓
Site office erection (Above-ground Works)			✓
Concrete paving (Above-ground Works)		✓	✓
Flood wall erection (Above-ground Works)		✓	✓
Alteration and Additional works inside the tunnel (Under-ground Works)			✓

Other factors that might affect the monitoring results	Reporting Period		
	November 2023	December 2023	January 2024
Non-project related construction activities in the adjacent construction sites	✓	✓	✓
Nearby residents' activities (e.g. renovation)		✓	

Appendix E Noise Monitoring Results and Graphic Presentation

Location CD5 - Multi-Welfare Services Complex							
Date	Weather	Time	Measure Level			Average Leq	Limit Level dB(A)
			Unit: dB (A) (5-mins)				
			Leq	L10	L90		
2024-1-02	Sunny	14:13	70.2	71.7	67.9	69.6	75
		14:18	69.6	71.1	67.6		
		14:23	68.3	69.5	66.8		
		14:28	68.6	70.0	67.1		
		14:33	70.7	71.6	67.6		
		14:38	69.7	71.6	67.6		
2024-1-08	Sunny	8:49	69.1	70.4	67.4	70.0	75
		8:54	69.0	70.3	67.3		
		8:59	69.2	70.4	67.6		
		9:04	72.0	74.0	68.0		
		9:09	69.6	71.1	67.7		
		9:14	70.0	71.1	68.4		
2024-1-19	Sunny	11:22	70.8	72.4	65.6	70.4	75
		11:27	73.6	77.9	63.7		
		11:32	71.7	75.0	65.9		
		11:37	68.3	70.9	63.7		
		11:42	66.4	68.7	61.8		
		11:47	67.5	70.2	63.3		
2024-1-25	Fine	9:29	71.0	72.8	68.8	72.0	75
		9:34	71.7	72.9	69.4		
		9:39	72.6	74.2	70.0		
		9:44	72.2	73.8	70.2		
		9:49	71.4	72.7	69.6		
		9:54	72.6	74.4	70.3		
2024-1-31	Sunny	9:21	73.1	75.1	69.0	73.7	75
		9:26	73.4	75.9	70.0		
		9:31	73.6	75.7	70.2		
		9:36	74.4	75.2	70.8		
		9:41	73.3	75.4	69.3		
		9:46	74.1	76.7	69.2		

Noise Monitoring Results

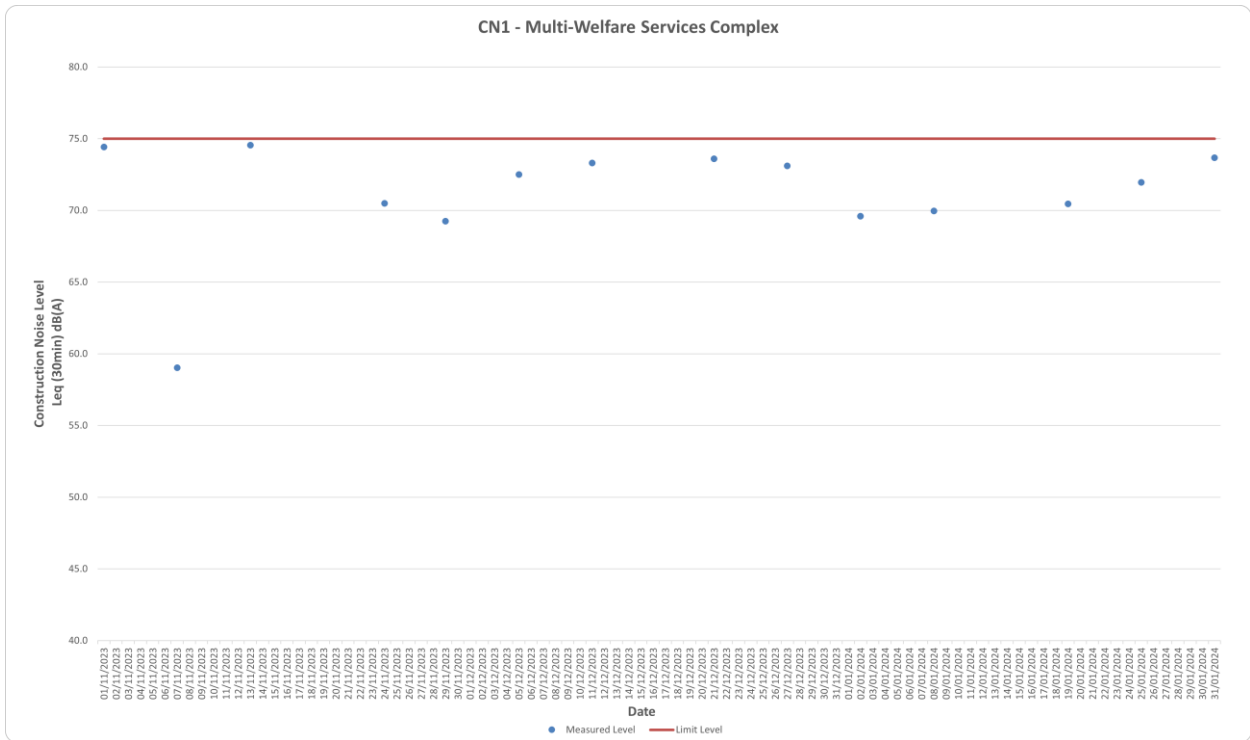

Major Construction Activities	Reporting Period		
	November 2023	December 2023	January 2024
Site clearance (Above-ground Works)	✓	✓	
Site installation (Above-ground Works)	✓	✓	✓
Haul road formation (Above-ground Works)	✓	✓	✓
Hoarding erection (Above-ground Works)	✓	✓	✓
Site office erection (Above-ground Works)			✓
Concrete paving (Above-ground Works)		✓	✓
Flood wall erection (Above-ground Works)		✓	✓
Alteration and Additional works inside the tunnel (Under-ground Works)			✓

Other factors that might affect the monitoring results	Reporting Period		
	November 2023	December 2023	January 2024
Non-project related construction activities in the adjacent construction sites	✓	✓	✓
Nearby residents' activities (e.g. renovation)		✓	

Appendix F Weather Condition


Date	Mean Pressure (hPa)	Air Temperature			Mean relative Humidity (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)		
January 2024						
1	1019.9	22	19.9	18.8	75	0
2	1019.1	20.5	18.7	17.8	76	0
3	1020	21.6	18.8	15.7	64	0
4	1020.9	19.6	17	15.4	67	0
5	1020.2	22	18.8	16.6	75	0
6	1020.1	23.8	20.2	17.8	76	0
7	1021	21.8	19.9	18.6	71	0
8	1019.6	20.6	19.1	17.7	73	Trace
9	1017.2	23.9	20.5	18.1	77	Trace
10	1018.6	23.2	20.3	17.9	67	0
11	1020	21.5	18.9	17.6	69	Trace
12	1019.1	21.8	18.9	17.1	75	0
13	1019.9	22	19.6	17.8	57	0
14	1021.1	23.8	20.7	18.5	56	0
15	1021.2	24.8	20.9	18.8	71	0
16	1022.1	20.5	18.7	17.5	75	0
17	1020.4	20.6	19.2	17.7	72	0.1
18	1017.7	24.2	21.2	19.1	74	0
19	1016.3	24.2	21.1	19.2	76	0
20	1016.3	24.6	21.4	19.5	75	0
21	1020.3	21.3	19.1	16.3	68	Trace
22	1023.3	18.5	15	9.8	72	0.5
23	1028.5	10.4	7.9	6.3	75	2.7
24	1029.2	12.5	9.2	6.5	59	0
25	1028.7	15.5	12.3	9.5	56	0
26	1027.3	17.8	15	13.1	61	0
27	1025.8	18.8	15.5	13.1	67	1
28	1026.4	15.7	13.7	11.7	83	2.4
29	1023.4	17.8	15.9	14.3	82	Trace
30	1020.7	20.2	18.3	16.8	88	Trace
31	1019.4	20.2	19.3	17.9	92	Trace

Remark: Trace means rainfall less than 0.05 mm


Source: Hong Kong Observatory

02 January 2024


Temperature/Humidity:

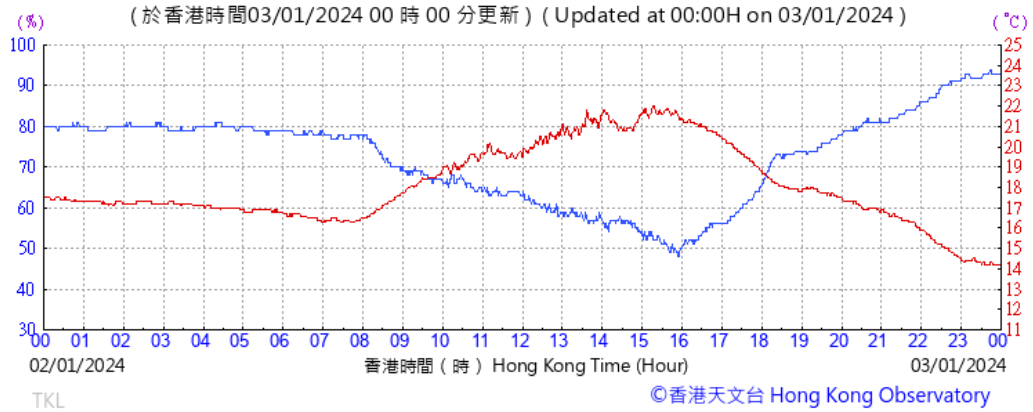

Pressure:

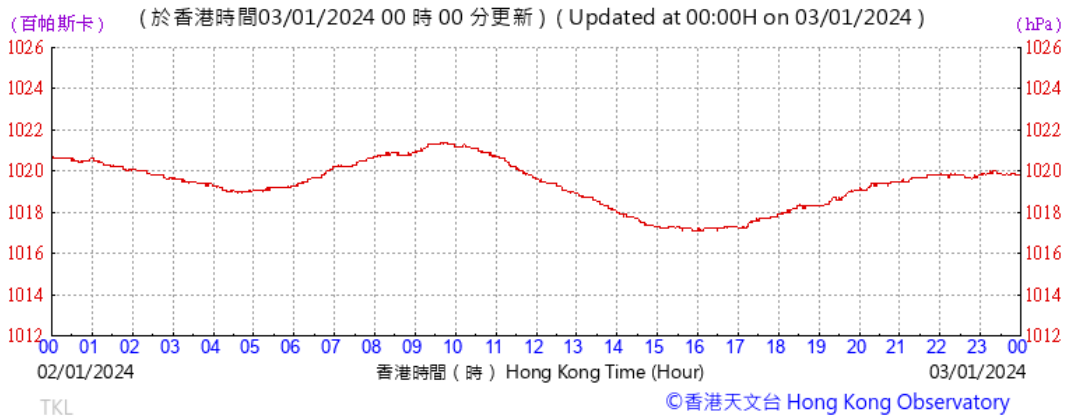

Wind Direction:

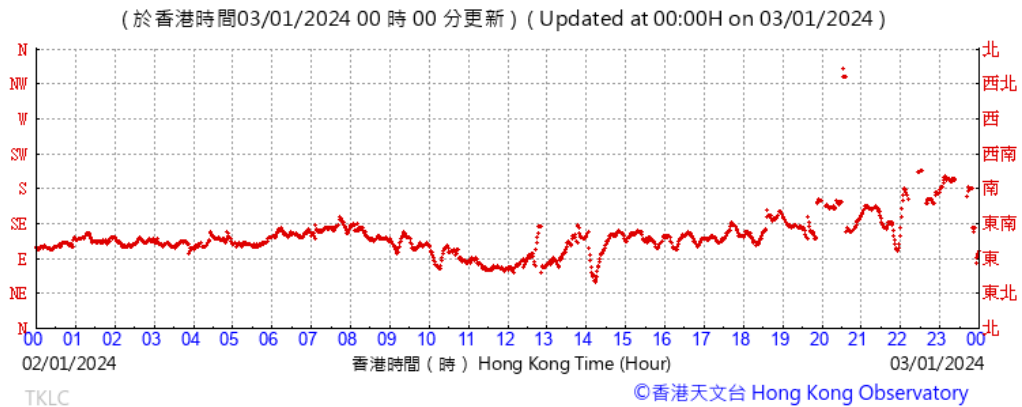


Wind Speed:




08 January 2024


Temperature/Humidity:

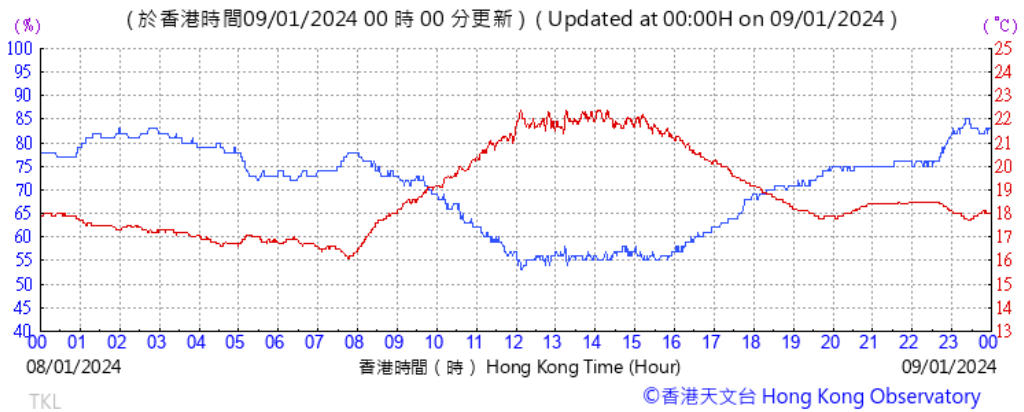


Pressure:

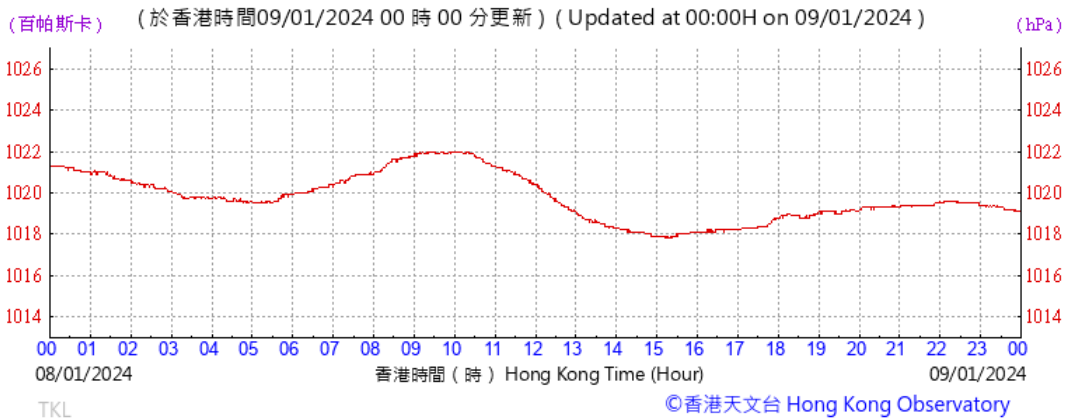

Wind Direction:

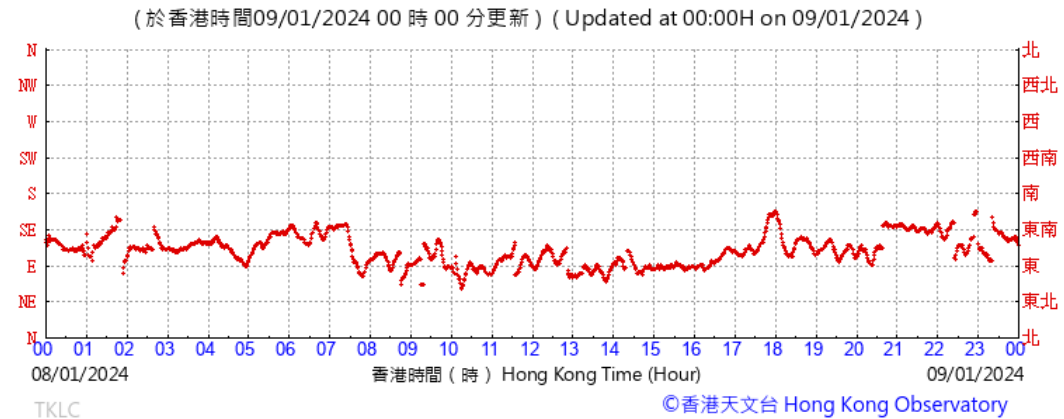


Wind Speed:

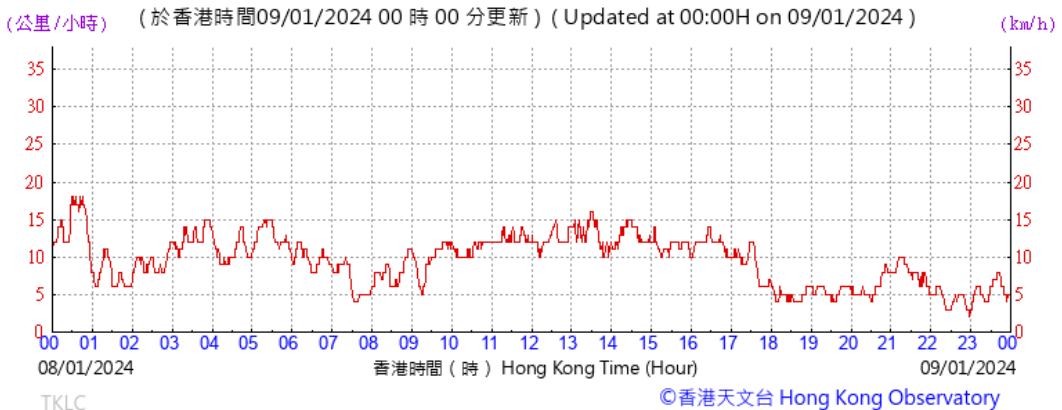


13 January 2024


Temperature/Humidity:

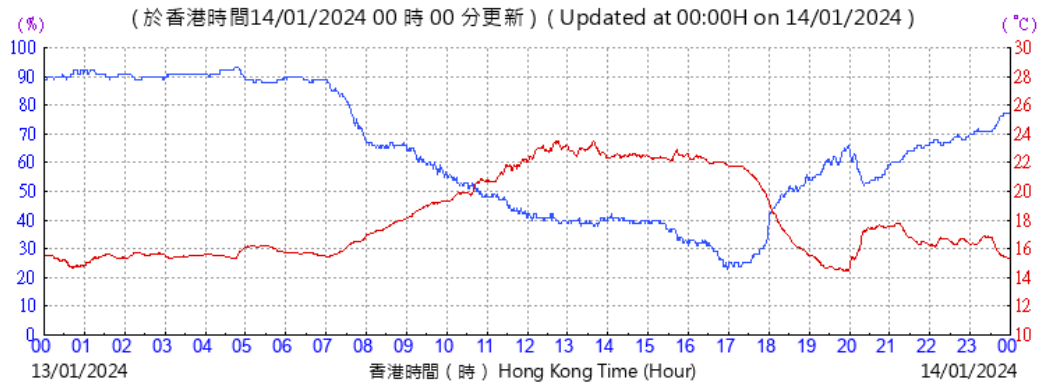


Pressure:

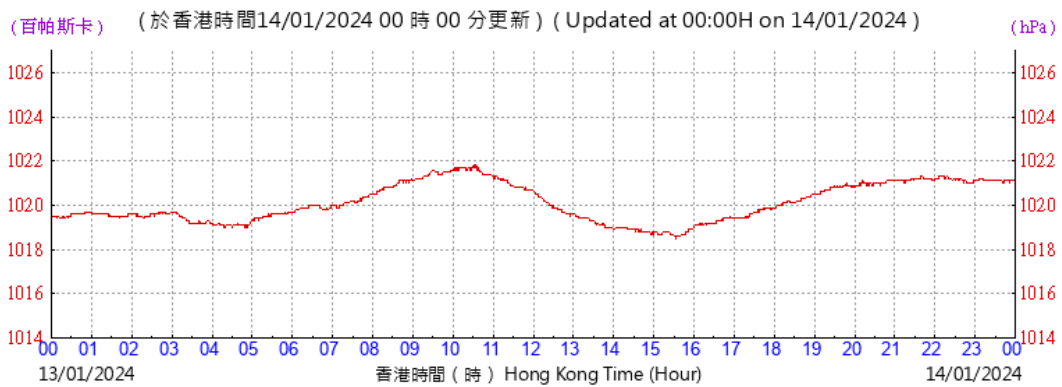



Wind Direction:

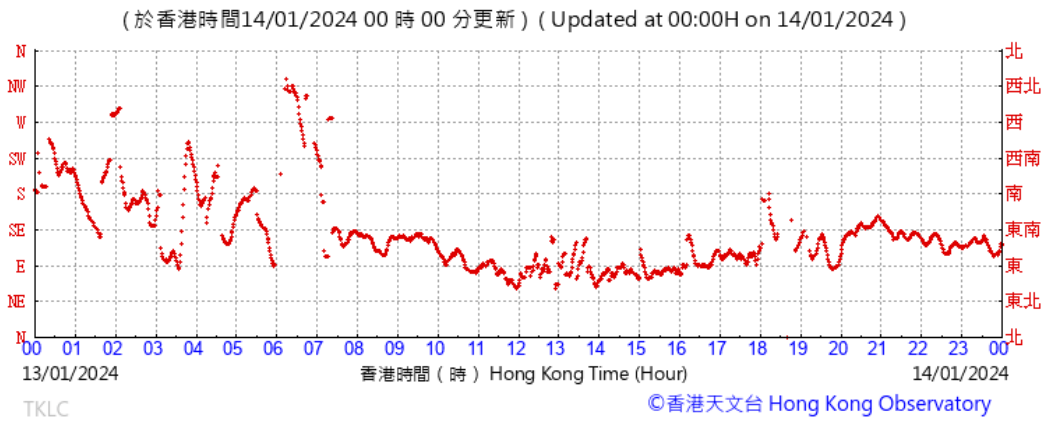

Wind Speed:

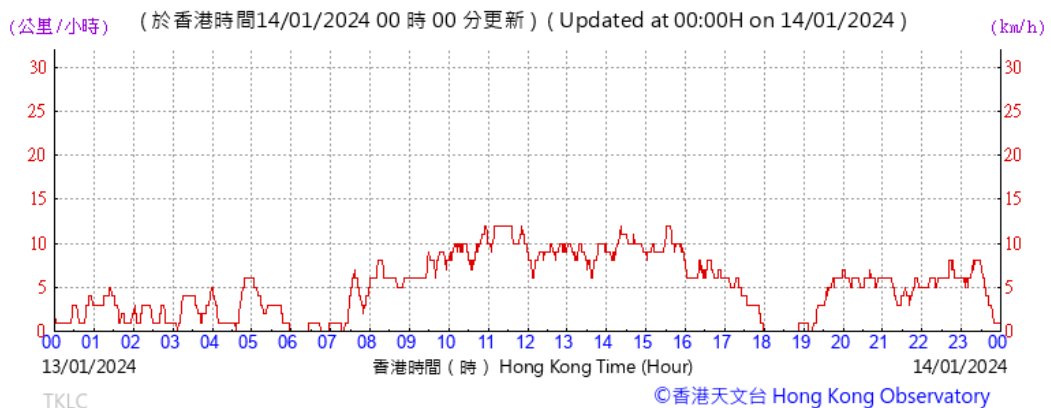

19 January 2024

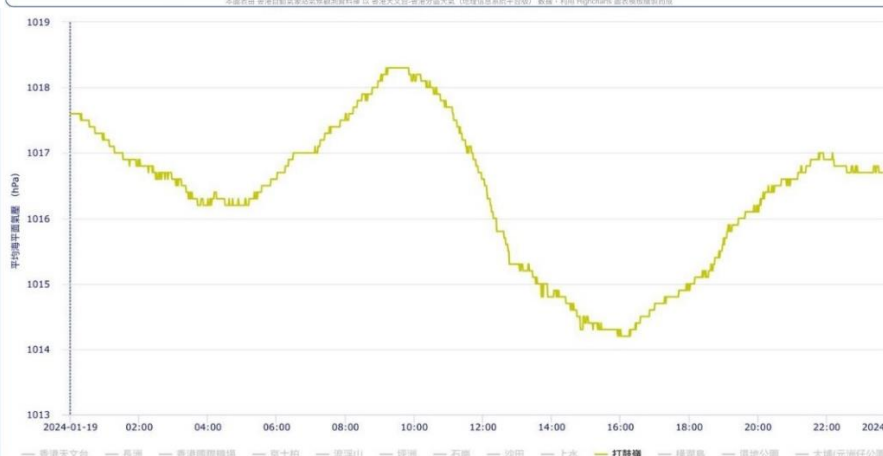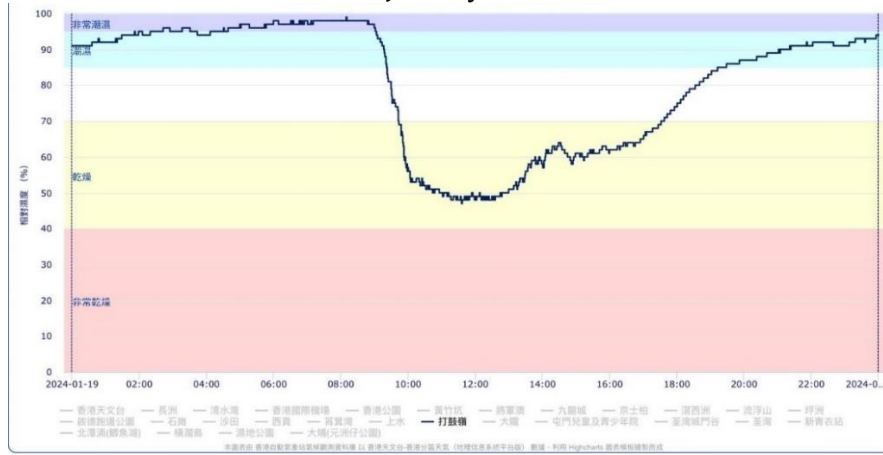


Wind Direction data is not available.

Source: i-lens.hk


Link: https://i-lens.hk/hkweather/instant_chart.php

25 January 2024


Temperature/Humidity:

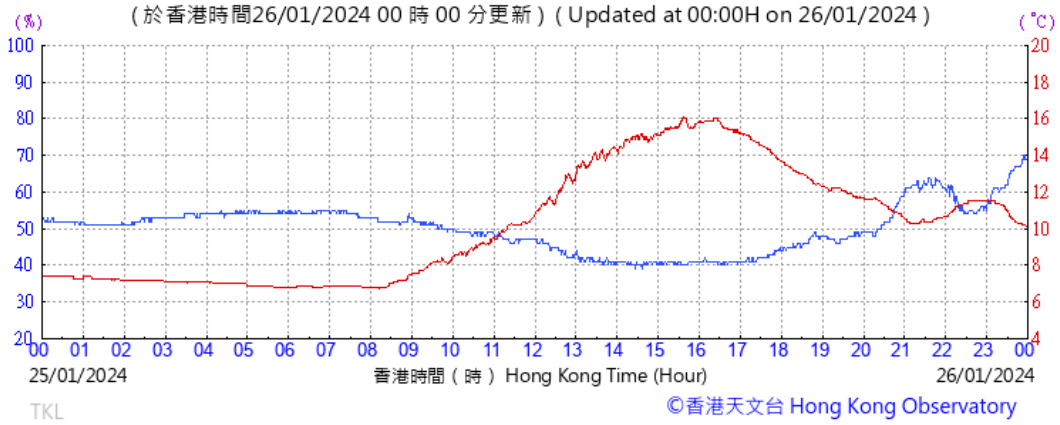


Pressure:

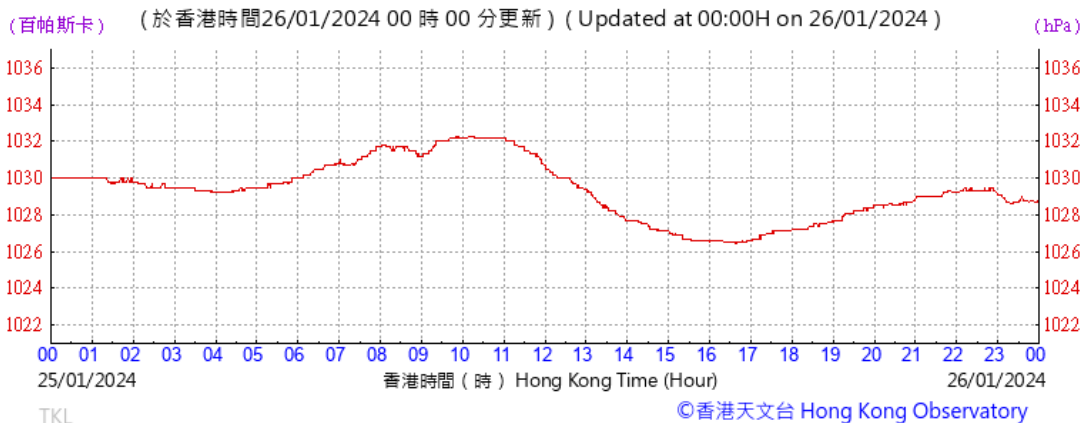

Wind Direction:

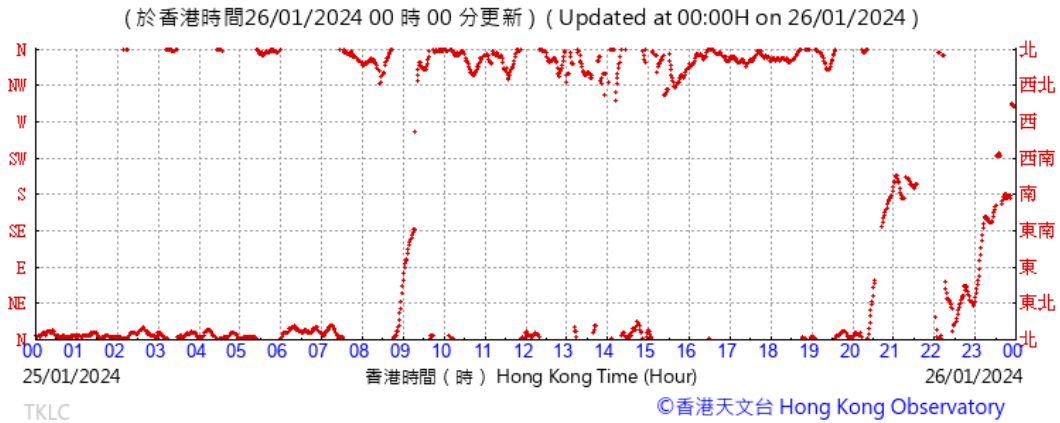


Wind Speed:

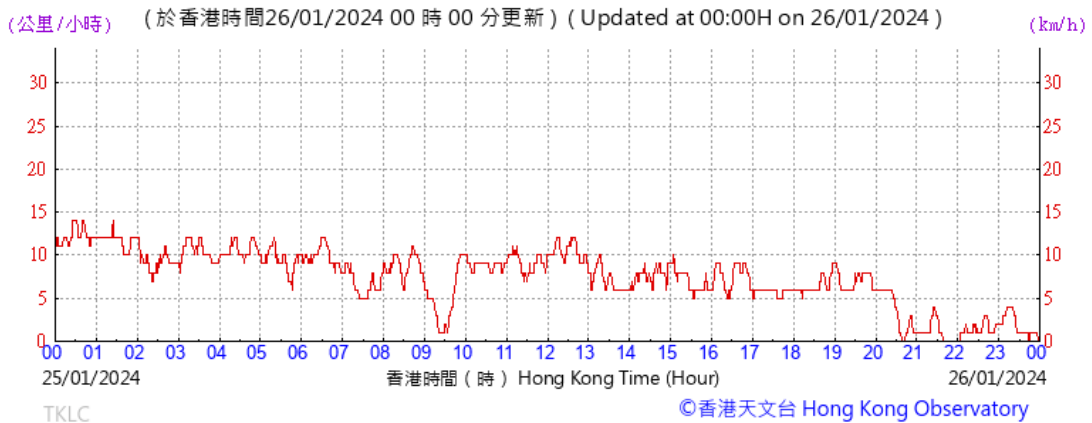


31 January 2024


Temperature/Humidity:

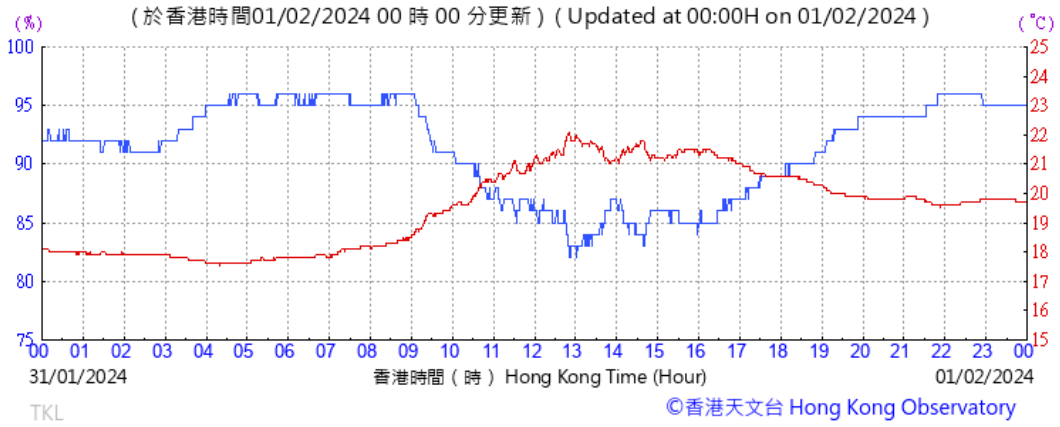

Pressure:

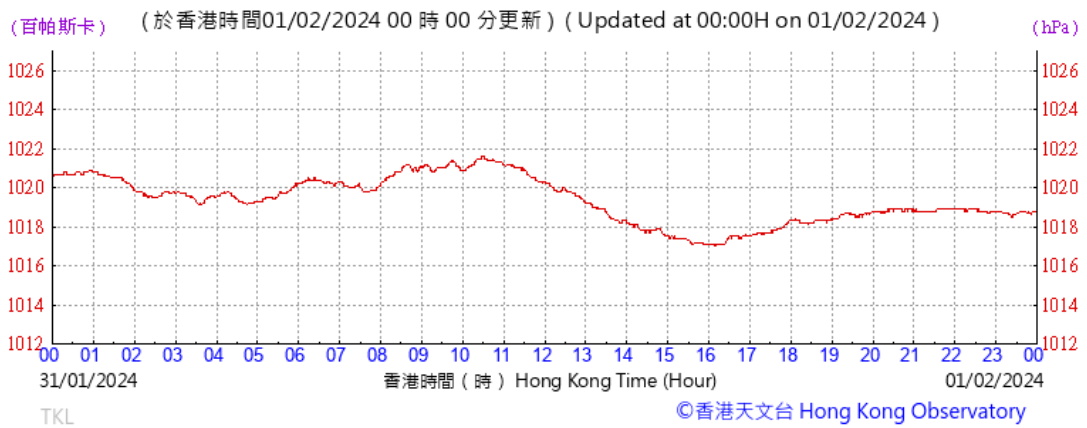

Wind Direction:

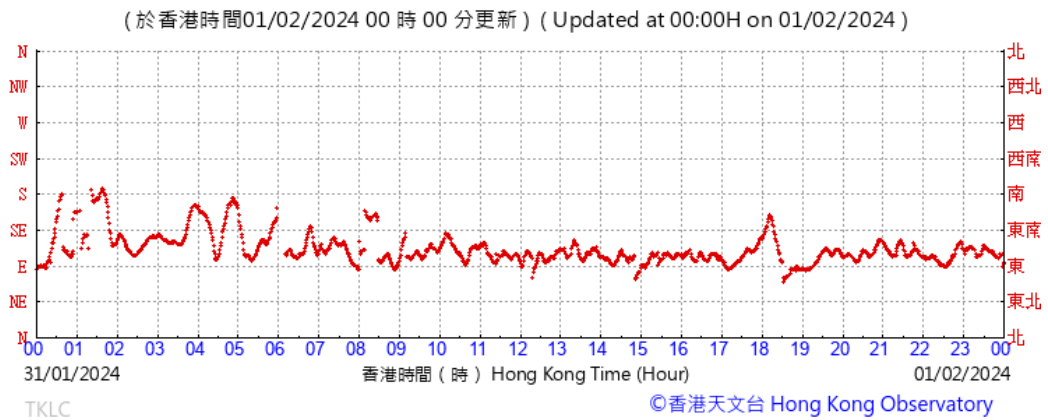

Wind Speed:



Appendix G Event and Action Plan

Event and Action Plan for Construction Dust

Event	Action			
	ET	IEC	ER	Contractor
Action level exceedance for one sample	<ol style="list-style-type: none"> 1. Repeat measurement to confirm finding; 2. If exceedance is confirmed, inform Contractor, IEC and ER; 3. Identify source, investigate the causes of exceedance and propose remedial measures; 4. Discuss with the Contractor, IEC and ER on the remedial measures required; 5. Increase monitoring frequency. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing. 	<ol style="list-style-type: none"> 1. Identify source(s), investigate the causes of exceedance and propose remedial measures; 2. Implement remedial measures; 3. Amend working methods agreed with the ER as appropriate.
Action level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Repeat measurement to confirm finding; 2. If exceedance is confirmed, inform Contractor, IEC and ER; 3. Identify source, investigate the causes of exceedance and propose remedial measures; 4. Advise the Contractor and ER on the effectiveness of the proposed remedial measures; 5. Increase monitoring frequency; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER to discuss the remedial measures to be taken; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. In consultation with the ET and IEC agree with the Contractor on the remedial measures to be implemented; 3. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Identify source(s), investigate the causes of exceedance and propose remedial measures; 2. Submit proposals for remedial measures to the ER, ET and IEC within three working days of notification for agreement; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Limit level exceedance for one sample	<ol style="list-style-type: none"> 1. Repeat measurement to confirm finding; 2. If exceedance is confirmed, inform IEC, ER, Contractor and EPD; 3. Increase monitoring frequency to daily; 4. Discuss with the ER, IEC and Contractor on the remedial measures and assess effectiveness; 5. Keep ER, IEC and EPD informed of the results of the effectiveness of remedial measures. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Review and agree on the remedial measures proposed by the Contractor; 3. Ensure remedial measures properly implemented; 4. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Identify source(s), investigate the causes of exceedance and propose remedial measures 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER, ET and IEC within three working days of notification for agreement; 4. Implement the agreed proposals; 5. Amend proposal if appropriate.

Event and Action Plan for Construction Dust

Event	Action			
	ET	IEC	ER	Contractor
Limit level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Repeat measurement to confirm finding; 2. If exceedance is confirmed, inform IEC, ER, Contractor and EPD; 3. Increase monitoring frequency to daily; 4. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 5. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 6. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET 2. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 3. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; 3. Supervise the implementation of remedial measures; 4. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source(s), investigate the causes of exceedance and propose remedial measures 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER, IEC and ET within three working days of notification for agreement; 4. Implement the agreed proposals; 5. Review and resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer or Engineer's Representative

Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> 1. Notify IEC, ER and Contractor; 2. Identify source and carry out investigation; 3. Discuss with the Contractor and formulate remedial measures; 4. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Identify source, and carry out investigation and report the investigation to the ET, IEC and ER; 2. Submit noise mitigation proposals to IEC and ER; 3. Implement noise mitigation proposals.
Limit Level Exceedance	<ol style="list-style-type: none"> 1. Repeat measurements to confirm exceedance; 2. If exceedance is confirmed, notify the Contactor, IEC, EPD and ER; 3. Increase monitoring frequency; 4. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 5. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 6. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring results and discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Ensure remedial measures properly implemented; and 3. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source and carry out investigation and report the investigation to the ET, IEC and ER; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER, ET and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix H Summary of Exceedance

Exceedance Report for Air Quality

Location	Parameter	No. of exceedance in the reporting period		No. of accumulated exceedance	
		Action Level	Limit Level	Action Level	Limit Level
CD1a	1-hr TSP	0	0	0	0
CD2a		0	0	0	0
CD3a		0	0	0	0
CD4a		0	0	0	0
CD5		0	0	0	0

Exceedance Report for Construction Noise

Location	Parameter	No. of exceedance in the reporting period		No. of accumulated exceedance	
		Action Level	Limit Level	Action Level	Limit Level
CN1	L_{eq} (30-mins) dB(A)	0	0	0	0

Appendix I Environmental Mitigation Implementation Schedule (EMIS)

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
<i>Construction Dust Impact</i>								
S7.5.3	D1	<p>The following dust suppression measures/practices should be incorporated:</p> <ul style="list-style-type: none"> • undertaking at all times to prevent dust nuisance as a result of the activities. Effective dust suppression measures, as necessary, should be installed to minimise air quality impacts, at the boundary of the site and at any sensitive receivers. • Frequently cleaning and watering the site to minimise fugitive dust emissions. • Effective water sprays shall be used during the delivery and handling of all raw sand, aggregate and other similar materials, when dust is likely to be created, to dampen all stored materials during dry and windy weather. • Watering of exposed surfaces shall be conducted as often as possible depending on the circumstances. • Areas within the site where there is a regular movement of vehicles shall have an approved hard surface, be kept clear of loose surface materials and / or regularly watered. • Where dusty materials are being discharged to vehicle from a conveying system at fixed transfer point, a three-sided roofed enclosure with a flexible curtain across the entry shall be provided. Exhaust fans shall be provided for this enclosure and vented to a suitable fabric filter system. • Confine haulage and delivery vehicles to designated roadways inside the site. If in the opinion of the Engineer, any motorised vehicle is causing dust nuisance, the Engineer may require that the vehicle be restricted to a maximum speed of 15 km per hour while within the site area. 	Minimise dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> • APCO • To control the dust impact to meet HKAQO and EIAOTM 	<p>Implemented</p> <p>Implemented after observation</p> <p>N/A</p> <p>Implemented after observation</p> <p>Implemented</p> <p>N/A</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> • Wheel cleaning facilities shall be installed and used by all vehicles leaving the site. No earth, mud, debris, dust and the like shall be deposited on public roads. Water in the wheel cleaning facility shall be changed at frequent intervals and sediments shall be removed regularly. The Contractor shall submit details of proposals for the wheel cleaning facilities to the Engineer prior to construction of the facility. Such wheel cleaning facilities shall be usable prior to any earthwork excavation activity on site. The Contractor shall provide a hard-surfaced road between any cleaning facility and the public road. • Any stockpile of dusty material shall be either: a) covered entirely by impervious sheeting; b) placed in an area sheltered on the top and the three sides; or c) sprayed with water so as to maintain the entire surface wet. • Chemical wetting agents shall only be used on completed cuts and fills to reduce wind erosion. • All site vehicular exhausts should be directed vertically upwards or directed away from ground to minimise dust nuisance as far as practicable. • Ventilation system, equipped with proprietary filters, should be provided to ensure the safe working environment inside the tunnel. Particular attention should be paid to the location and direction of the ventilation exhausts. The exhausts should not be allowed to face any sensitive receivers directly. Consideration should also be given to the location of windows, doors and direction of prevailing winds in relation to the nearby sensitive receivers. 						<p>N/A</p> <p>Implemented after observation</p> <p>N/A</p> <p>N/A</p> <p>N/A</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<p>The following measures related to stockpiling, loading and unloading activities should be incorporated:</p> <ul style="list-style-type: none"> • The working area of any excavation or earthmoving operation shall spray with water immediately before, during and immediately after the operation so as to maintain the entire surface wet; • Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies; • Any stockpile of dusty materials shall be either covered entirely by impervious sheeting or placed in an area sheltered on the top and three sides; and sprayed with water so as to maintain the entire surface wet; and • Other suitable dust control measures as stipulated in the Air Pollution Control (Construction Dust) Regulation, where appropriate, should be adopted. 						<p>Implemented</p> <p>N/A</p> <p>Implemented after observation</p> <p>N/A</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
S7.5.3	D2	<p>The following good site practices to reduce the exhaust emission from the use of non-road mobile machinery and construction plant and equipment should be implemented:</p> <ul style="list-style-type: none"> Regulated machines shall be used and exempted NRMMS should be avoided where practicable. Use cleaner fuel such as Ultra Low Sulphur Diesel (ULSD) in diesel-operated construction plant to reduce sulphur dioxide emission. Use of electric PMEs where practicable. Use power supplied from power utilities when practicable (e.g. to replace generators). Switch off the engine of PMEs when idling. Implement regular and proper maintenance for plant and equipment. Employ plant and equipment of adequate size and power output and avoid overloading of the plant. Locate the PMEs away from sensitive receivers as far as possible. Erect screen to shield the emission source from sensitive receivers where necessary and practicable. 	Control emissions from non-road mobile machinery	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Air Pollution Control (NRMMS) (Emission) Regulation To control the fuel combustion emission from PMEs 	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>N/A</p>
S14.3.3.4	D3	Implement regular dust monitoring under EM&A programme during the construction phase.	Monitoring impact of dust	Contractor	Selected dust monitoring stations	Construction phase	• EIAO-TM	Implemented
Construction Noise								
S8.4.4.1	N1	The following good site practices to reduce the noise impact from construction site activities, the following measures should be implemented:	Control construction airborne noise	Contractor	All construction sites	Construction phase	• Annex 5, EIAO-TM	

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> only well-maintained plant should be operated onsite and plant should be serviced regularly during the construction programme; machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; silencers or mufflers which available on construction equipment should be properly fitted and maintained during the construction works; spoil transportation routes should be directed away from NSRs as far as practicable; mobile plant should be sited as far away from NSRs as possible and practicable; material stockpiles, site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities; noise monitoring at selected NSRs should be conducted as far as practicable; and provide designated unloading areas away from the NSR as far as possible. 						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>N/A</p> <p>Implemented</p> <p>Implemented</p> <p>N/A</p> <p>Implemented</p> <p>Implemented</p>
S8.4.4.2	N2	Use of quiet plant, where necessary should be made reference to the Powered Mechanical Equipment (PME) listed in the Technical Memorandum or the Quality Powered Mechanical Equipment (QPME) / other commonly used PME listed in Environmental Protection Department (EPD) web pages as far as possible which includes the Sound Power Level (SWLs) for specific quiet PME	Reduce the noise levels from plant items	Contractor	All construction sites where practicable	Construction phase	<ul style="list-style-type: none"> Annex 5, EIAO-TM PN 1/24 	Implemented

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
S8.4.4.3	N3	Install movable temporary noise barriers (typical design is material surface density of 10kg/m ² could achieve at least 5dB(A) reduction for movable plant and 10dB(A) for stationary plant.), and full enclosure, screen the noisy plants including air compressor and generator etc.	Minimise the construction noise levels through screening	Contractor	All construction sites	Construction phase	• Annex 5, EIAO-TM	N/A
S14.3.3.5	N4	Implement regular airborne construction noise monitoring under EM&A programme.	Monitor the airborne construction noise levels at the selected representative locations	Contractor	Proposed noise monitoring stations	Construction phase	• Annex 5, EIAO-TM	Implemented
Operational Fixed Plant Noise								
S8.5.2.1	N5	Housing all noisy equipment inside the plantroom with sufficient sound insulation and sound attenuators for all air louvers (e.g. install plant rooms with fresh air louvres, exhaust air louvres, smoke discharge louvres, etc.) in order to reduce the typical planned fixed noise sources for railway station at the proposed entrances (incorporated with VB) and proposed FRS, including ventilation fans, smoke extraction fans, chillers etc.	Minimise the operational fixed plant noise	Contractor	Construction of railway station at the proposed entrances (incorporated with VB) and proposed FRS	Operational phase	• Annex 5, EIAO-TM	N/A
S8.5.2.2	N6	The following good site practices to reduce the noise impact on fixed noise sources, the following measures shall be considered as far as practicable to minimise any potential impacts: • Equipment should be placed in a plant room with thick walls or at a much greater distance from the receiver or behind some large enough obstruction (e.g. a building or a barrier);	Control the operational fixed plant noise	Contractor	Construction of railway station at the proposed entrances (incorporated with VB) and proposed FRS	Operational phase	• Annex 5, EIAO-TM	N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> Quieter plant should be chosen as far as practicable; Noise levels specification should be included when ordering new plant items; All openings, including louvres for ventilation and machine room doors should be oriented away from the NSRs as far as practicable; Silencers, acoustic louvres or acoustic doors should be used where necessary; and Regularly scheduled plant maintenance programme should be developed and implemented so that plant items are properly operated and serviced. 						<p>Implemented</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p>
S14.3.3.5	N7	Fixed plant commissioning tests shall be conducted for each planned fixed noise source.	To ensure the compliance of predicted the maximum allowable Sound Power Level	Contractor/ MTR Corporation	Each planned fixed noise source	Prior to operational phase	<ul style="list-style-type: none"> NCO EIAO-TM 	N/A
Water Quality (Construction Phase)								
S9.3.2.2	W1	<p><u>General Construction Activities</u></p> <p>Best Management Practices (BMPs) should be implemented as far as practicable according to The Professional Persons Environmental Consultative Committee (ProPECC) Practice Note (PN) 2/23 “Construction Site Drainage”. The details of BMPs are presented as follows:</p> <ul style="list-style-type: none"> The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 2/23. The detailed design of the sand/silt traps should be undertaken by the contractor prior to the commencement of construction; 	To reduce water quality impact from construction site runoff and general construction activities	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WPCO ProPECC (PN2/23) EIAO-TM DSS-TM Technical Circular No. 1/2017 Practical Notes No. 1/2017 	N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> • Schedule construction works to minimise surface construction works during the rainy seasons (April to September). If excavation of spoil cannot be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion, temporary exposed slope surfaces shall be covered e.g. by tarpaulin, and temporary access roads shall be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels shall be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements shall always be in place in such a way that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm; • Inspect and maintain all drainage facilities and erosion and sediment control structures regularly to ensure proper and efficient operation at all times and particularly following rainstorms; • Cover all construction materials at temporary storage area with tarpaulin or similar fabric, and temporary access roads shall be protected by crushed stone or gravel, as excavation proceeds during rainstorms and implementation of measures to prevent the washing away of construction materials, soil, silt or debris into any drainage system; • Intercepting channels shall be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces during rainstorm; • Cover manholes (including newly constructed ones), if any, adequately and seal temporarily to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers; 						<p>N/A</p> <p>Implemented</p> <p>N/A</p> <p>N/A</p> <p>N/A</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> Take precautions at any time of year when rainstorms are likely. The actions to be taken based on the guidelines in Appendix A2 of ProPECC PN 2/23; Collect, handle and dispose construction solid waste, debris and rubbish on site to avoid water quality impacts; Provide locks for all fuel tanks and storage areas and locate on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby; and Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, marsh and ponds. 						<p>N/A</p> <p>Implemented</p> <p>N/A</p> <p>Implemented</p>
S9.3.2.1	W2	<u>Mitigation measures/ enhancement measures during demolition of watercourse</u> <ul style="list-style-type: none"> any surface runoff would be diverted by temporary drain or pumped away and treated by sedimentation tanks before discharge. All discharge to stormwater drain should be followed discharge licence under the Water Pollution Control Ordinance (WPCO) 	To avoid the untreated surface run-off being accidentally discharged into the adjoining water bodies.	Contractor	watercourse	Construction phase	<ul style="list-style-type: none"> WPCO ProPECC (PN2/23) EIAO-TM DSS-TM 	<p>N/A</p> <p>N/A</p>
S9.3.2.3	W3	<u>Mitigation measures for effluent discharge from excavation</u> <ul style="list-style-type: none"> Wastewater from excavation with a high level of suspended solids should be filtered before discharge by settlement in tanks with sufficient retention time. 	To minimize the water quality impact from the	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WPCO ProPECC (PN2/23) 	N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> All discharge to stormwater drain should be followed discharge licence under the Water Pollution Control Ordinance (WPCO) The contractor should be monitor the quantity and quality of effluent discharge to ensure compliance with the conditions of the discharge license 	wastewater generated form excavation				<ul style="list-style-type: none"> EIAO-TM DSS-TM 	N/A
								N/A
S9.3.2.4	W5	<u>Sewage Effluent from Construction Workforce</u> <ul style="list-style-type: none"> No discharge of sewage to the stormwater system and marine water will be allowed; Establish adequate and sufficient portable chemical toilets in the works areas to handle sewage from the construction workforce; Employ a licenced waste collector to clean and maintain the chemical toilets on a regular basis; and Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the surrounding environment. 	To reduce water quality impact from wastewater from construction workforce.	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WPCO ProPECC (PN2/23) EIAO-TM DSS-TM 	Implemented Implemented Implemented Implemented
S9.3.2.5	W6	<u>Accidental Spillage</u> <ul style="list-style-type: none"> Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities; Any chemical waste generated shall be managed in accordance with the Waste Disposal (Chemical Waste) (General) Regulation; The Contractor should develop management procedures for chemicals used and prepare an emergency spillage handling procedure to deal with chemical spillage in case of an accident occurs; 	To minimise water quality impact from accidental spillage of chemicals	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WPCO ProPECC (PN2/23) EIAO-TM DSS-TM WDO 	Implemented Implemented N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> • Any services and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with the potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges; • The service and maintenance as well as any chemical storage area would be avoided to position near the watercourse as a safe guard; • The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance shall be followed to deal with chemical wastes; • Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling, and transport; • Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and • Storage area should be selected at a safe location on-site and adequate space should be allocated to the storage area. 						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>N/A</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
<i>Water Quality (Operational Phase)</i>								
S9.4.2.1	W7	<p><u>The following mitigation measures for stormwater surface runoff will be implemented.</u></p> <ul style="list-style-type: none"> Stormwater surface runoff generated should be discharged to the nearby government drainage system. The rainwater runoff from station structures (e.g. ventilation building, entrance, etc.) is provided with peripheral drain conveying to government drainage. 	To minimize the water quality impact from stormwater surface runoff	MTR Corporation	Whole alignment	Operational Phase	<ul style="list-style-type: none"> WPCO 	N/A N/A
S9.4.2.2	W8	<p><u>The following mitigation measures for sewage and other wastewater will be implemented.</u></p> <ul style="list-style-type: none"> Sewage effluents including the sewage from the sanitary fitment and the foul water from washing facilities and track of the proposed railway station at Kwu Tung should be conveyed to the public sewers. During the interim phase, the sewage will be connecting to the public sewer at the west. As for the ultimate phase, the sewage will be conveyed to the public sewer along Road L3 of Kwu Tung North New Development Area. Standard oil/grit interceptors/chambers should be provided where necessary to remove the oil, lubricants, grease, silt, and grit from wastewater generated from facilities washing before discharge to public sewers. A discharge licence for the discharge of commercial and industrial effluent is needed and the discharge quality must satisfy all the standards listed in the DSS-TM and meet the requirements specified in the discharge licence. The practices outlined in ProPECC PN 1/23 for handling, treatment, and disposal of operational stage effluent should also be adopted where applicable. 	To minimize the water quality impact from sewage and other wastewater	MTR Corporation	Whole alignment	Operational Phase	<ul style="list-style-type: none"> WPCO ProPECC PN 1/23 DSS-TM 	N/A N/A N/A N/A N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
Waste Management (Construction Phase)								
S10.2.2.1	WM1	<p>Good Site Practices</p> <p>The following good site practices are recommended to reduce waste generation during construction:</p> <ul style="list-style-type: none"> • Nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all waste generated at the site; • Training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; • Provision of sufficient waste disposal points and regular collection for disposal; • Appropriate measures to minimise windblown litter and dust during transportation of waste by transporting waste in enclosed containers; • Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and • A Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP) should be prepared by the Contractor in accordance with ETWB TC(W) No.19/2005 and submitted to the Engineer for approval before construction works. 	Ensure proper waste management system throughout the construction	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> • WDO • ETWB TC(W) 19/2005 	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
S10.2.2.2	WM2	<p><u>Waste Reduction Measures</u></p> <p>The following recommendations are proposed to achieve reduction of waste:</p> <ul style="list-style-type: none"> • Segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; • Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste; • Sort out demolition debris from demolition works to recover reusable/ recyclable portions (i.e. Soil, broken concrete, metal etc.); and • Provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	All construction sites	Construction phase	• WDO	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S10.2.2.3	WM3	<p><u>Storage, Collection and Transportation of Waste</u></p> <p>The following recommendation should be implemented to minimise the impacts from storage, collection and transportation of waste:</p> <ul style="list-style-type: none"> • Non-inert C&D materials (if any) should be handled and stored well to ensure secure containment; • Stockpiling area should be provided with covers and water spraying system to prevent materials from windblown or being washed away; • Different locations should be designated to stockpile each material to enhance reuse; • Remove waste in timely manner; 	Minimise impact to the environment due to storage, collection and transport of waste	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> • WDO • Land (Miscellaneous Provisions) Ordinance • ETWB TCW No. 19/2005 	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> Employ the trucks with cover or enclosed containers for waste transportation; Obtain relevant waste disposal permits from the appropriate authorities; and Disposal of waste should be done at licensed waste disposal facilities. 						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S10.2.2.4	WM4	<p><u>C&D Materials</u></p> <p>The following recommendation should be implemented in handling the C&D materials:</p> <ul style="list-style-type: none"> Carry out on-site sorting; Allow and promote the use of recycled aggregates where appropriate; and Implement a trip-ticket system in accordance with DEVB TC(W) No. 6/2010 Trip Ticket System for Disposal of Construction and Demolition Materials, if dumping trucks are required, for each works contract to ensure that the disposal of C&D materials is properly documented and verified. <p><u>On-site Sorting of C&D Materials</u></p> <ul style="list-style-type: none"> Storage areas would be located within the site during construction phase for temporary storage of inert C&D materials. All C&D materials arising from the construction would be sorted on-site to recover the inert C&D materials and reusable and recyclable materials prior to disposal off-site. Non-inert portion of C&D materials should also be reused whenever possible and be disposed of at landfills as a last resort. 	Minimize waste impacts from C&D materials handling	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WDO ETWB TCW No. 19/2005 Land (Miscellaneous Provisions) Ordinance 	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> The Contractor would be responsible for devising a system to work for on-site sorting of C&D materials and promptly remove all sorted and processed material arising from the construction activities to minimise temporary stocking on-site. It is recommended that the system should include the identification of the source of generation, estimated quantity, arrangement for on-site sorting and/ or collection, temporary storage areas, and frequency of collection by recycling Contractors or frequency of removal off-site. 						<p>Implemented</p> <p>Implemented</p>
S10.2.2.4	WM5	<u>Reuse of C&D Materials</u> <ul style="list-style-type: none"> Reuse suitable excavated rock by reworking at approved quarries (e.g. crushed as aggregates); Sorting of demolition debris and excavated materials from demolition works to recover reusable/ recyclable portions (e.g. soil, broken concrete, metal); and Protect recyclable material to keep it in usable condition. 	Minimize waste impacts from C&D materials handling	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WDO ETWB TCW No. 19/2005 Land (Miscellaneous Provisions) Ordinance 	<p>N/A</p> <p>Implemented</p> <p>N/A</p>
S10.2.2.4	WM6	<u>Specification of Inert C&D Materials to be Delivered Offsite</u> In case there are surplus inert C&D materials generated in the Project and are required to be delivered to the Public Fill Reception Facilities (PFRFs), the inert C&D materials should fulfil the following requirements: <ul style="list-style-type: none"> Reclaimed asphalt pavement will not be mixed with other materials when delivered to the public fill reception facilities; Moisture content of inert C&D materials will be lowered to 25% max. when delivered to the public fill reception facilities; 	Reduce waste generation	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> WDO ETWB TCW No. 19/2005 Land (Miscellaneous Provisions) Ordinance 	<p>N/A</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> Inert C&D materials delivered to the public fill reception facilities should be a size less than 250mm; and Inert construction waste shall not be in liquid form such that it can be contained and delivered by dump truck as far as possible. Inert C&D materials in liquid form shall be solidified before delivering to the public fill reception facilities. 						<p>Implemented</p> <p>Implemented</p>
S10.2.2.5	WM7	<p><u>Chemical Waste</u></p> <ul style="list-style-type: none"> For those processes which generate chemical waste, it may be possible to find alternatives to eliminate the use of chemicals, to reduce the generation quantities or to select a chemical type of less impact on environment, health and safety as far as possible. Wherever possible, opportunities for the reuse and recycling of materials will be taken. If chemical waste is produced at the construction site, the Contractors should register with EPD as chemical waste producers and follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Chemical waste should be stored in appropriate containers and collected by a licensed chemical waste collector. Chemical waste (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre (CWTC), or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. Any unused chemicals or those with remaining functional capacity should be collected for reuse as far as practicable. 	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Waste 	<p>N/A</p> <p>Implemented</p> <p>N/A</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
S10.2.2.6	WM8	<p><u>General Refuse</u></p> <ul style="list-style-type: none"> • General refuse should be stored in enclosed bins separately from construction and chemical wastes. • Recycling bins should also be placed to encourage recycling. • Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. • A reputable waste collector should be employed to remove general refuse on a regular basis. • Arrangements should be made with the recycling companies to collect the recycle waste as required. It is expected that such arrangements would minimize potential environmental impacts. • The Contractor should implement an education programme for workers relating to avoiding, reducing, reusing and recycling general waste. Participation in a local collection scheme should be considered by the Contractor to facilitate waste reduction. 	Minimise production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	• WDO	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
Waste Management (Operational Phase)								
S10.3.2.1	WM9	<u>General Refuse</u> <ul style="list-style-type: none"> Recycling of waste paper, aluminium cans and plastic bottles should be encouraged. It is recommended to place clearly labelled recycling bins at designated locations which could be accessed conveniently. General refuse should be separated from chemical waste by providing separated bins for storage to maximize the recyclable volume as far as practicable. A reputable waste collector should be employed to remove general refuse regularly to minimize odour, pest and litter impacts. Arrangements should be made with the recycling companies to collect the recycle waste as required. 	Remove municipal solid waste generated	MTR Corporation	Kwu Tung Station as well as associated facilities	Operational phase	• WDO	N/A N/A N/A N/A N/A
S10.3.2.2	WM10	<u>Chemical Waste</u> <ul style="list-style-type: none"> Subject to operational needs, if chemical waste is to be produced, the Project Proponent shall register with EPD as chemical waste producers as appropriate in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. Chemical waste should be collected and disposed of at appropriate facility like CWTC by licensed collectors. The requirements given in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes should be followed, where applicable, in handling of these chemical wastes. The requirements for the collection and disposal of chemical waste as stipulated in the Waste Disposal (Chemical Waste) (General) Regulation should be followed to monitor all movements of chemical wastes which will be collected by a licensed collector to a licensed facility for final treatment and disposal. 	Minimize production of chemical waste	MTR Corporation	All construction site	Operational phase	<ul style="list-style-type: none"> WDO Code of Practice on the Packaging, Labelling and Storage of Chemical Waste 	N/A N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> • Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. • Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidising, irritant, toxic, harmful, corrosive, etc. • Non-recyclable chemical waste (e.g. spent lubricant oil) should be disposed of at appropriate facility like CWTC by licensed collectors. Recyclable chemical waste (e.g. used fluorescent tubes) should be collected and transported off-site by licensed collectors. 						N/A N/A N/A
Cultural Heritage (Construction Phase)								
S12.3.1.2	CH1	AMO should be informed immediately in case of discovery of antiquities or supposed antiquities in the course of the project works in accordance with the Antiquities and Monuments Ordinance (Cap. 53), so that appropriate mitigation measures, if needed, can be timely formulated and implemented in agreement with AMO.	To timely formulate and implement appropriate mitigation measures for protection of archaeological remains if needed within all construction sites	Contractor/ MTR Corporation	All construction sites	Construction phase	• Antiquities and Monuments Ordinance (Cap. 53)	N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
S12.4	CH2	If there are any buildings / structures both at grade level and underground which were built on or before 1969 within the works sites/ works areas during the construction, the Project Proponent will alert AMO in an early stage or once identified.	To timely formulate and implement appropriate mitigation measures for protection of archaeological remains if needed within all construction sites	Contractor/ MTR Corporation	All construction sites	Construction phase	<ul style="list-style-type: none"> Antiquities and Monuments Ordinance (Cap. 53) 	N/A
Landscape and Visual (Construction Phase)								
S13.6.1	LV1	<u>Decorative Site Hoarding</u> Decorative site hoardings with aesthetic designs could be provided at the construction sites such that the construction site could be compatible with the surroundings and mitigate the visual impact.	Compatible with the surroundings and mitigate the visual impact.	Contractor	All construction sites	Construction Phase	<ul style="list-style-type: none"> EIAO-TM 	N/A
Landscape and Visual (Operational Phase)								
S13.6.2.2	LV2	<u>Compensatory Tree Planting</u> On-site and off-site tree compensation methods are being considered. The Project Proponent is still exploring the possible locations including the new development area at KTN NDA, LCSD park etc. of tree compensation and would continue to liaise with different government departments such as CEDD, LCSD, LandsD and AFCD etc. on the details for tree compensation. The following potential locations for tree compensation were identified and the actual locations are subject to further liaison with relevant parties:	Compensate for trees due to the Project	Contractor/ MTR Corporation	Onsite where possible. Otherwise consider offsite locations	Detailed design and operational phase	<ul style="list-style-type: none"> EIAO-TM DEVB TCW No. 4/2020 	N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
		<ul style="list-style-type: none"> Town Plaza in KTN NDA; LCSD sitting-out areas, parks, roadside tree pits and landscape areas in North District; Hillside in the North District for whip tree planting; and Any other locations to be agreed with government departments. 						N/A N/A N/A
S13.6.2.1	LV3	<p><u>Screen Planting/ Vertical Greening</u></p> <p>Screen planting/ vertical greening could effectively constitute a fascinating landscape and blend the building with the surrounding greenery.</p>	Improve compatibility with the surrounding environment	Contractor/ MTR Corporation	All structures as feasible, final location to be confirmed at detailed design phase	Detailed design and operational phase	<ul style="list-style-type: none"> EIAO-TM 	N/A
S13.7.2	LV4	<p><u>Architectural Aesthetic Design of Built Structure</u></p> <p>The design objectives are as follows:</p> <ul style="list-style-type: none"> To minimise the visual impact within a densely populated residential area by creating a simple and elegant design; To create a lean building massing, maximise the at grade green landscaping area to locals and minimise the visual impact; and To introduce biophilic orientated design as far as practicable. It is aimed to integrate the above-ground structures to the future landscape design by others and contributes to the immediate surroundings, such as green roofing, green wall, green fifth elevation design and environmentally sustainable architecture. 	Improve visual amenity of the built structure	Contractor/ MTR Corporation	All structures as feasible, final location to be confirmed at detailed design phase	Detailed design and operational phase	<ul style="list-style-type: none"> EIAO-TM 	N/A N/A N/A

ERR Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location /Timing	Implementation Phase	Requirements and / or standards to be achieved	Implementation Status
EM&A Project								
S14.3.1.4	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control EM&A performance	MTR Corporation	All construction sites	Construction Phase	<ul style="list-style-type: none"> EIAO Guidance Note No.4/2010 EIAO-TM 	Implemented
S14.3.1.3	EM2	<ul style="list-style-type: none"> An Environmental Team needs to be employed as per the EM&A Manual. An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	Perform environmental monitoring and auditing	Contractor/ MTR Corporation	All construction sites	Construction Phase	<ul style="list-style-type: none"> EIAO Guidance Note No.4/2010 EIAO-TM 	Implemented Implemented

Implementation status:	Responsibility	Description
	Implemented	Mitigation measure was fully implemented
	Implemented after Observation	Observation was made during site audit but improved/rectified by the contractor
	To be improved	Observation/reminder was made during last site audit but not yet improved/rectified by the contractor
	NC	Non-compliance of mitigation measure
	Rectified	Non-compliance but rectified by the contractor
	N/A	Not Applicable at this stage as no such site activities were conducted in the reporting period. The mitigation measure will be implemented when appropriate

Appendix J Waste Flow Table for Reporting Month

MONTHLY SUMMARY WASTE FLOW TABLE

YEAR: 2024

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity of Inert C&D Material Generated (A+B+C)	Reused in the Contract (A)	Reused in other Project (B)	Disposed at Public Fill (C)	Imported Fill	Metal	Paper/ cardboard packaging	Plastic	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000m ³)
Jan	0.1682*	0.0000	0.0000	0.1682*	0.0000	0.0000	0.0000	0.0000	0.0000	0.0219*
Feb	-	-	-	-	-	-	-	-	-	-
Mar	-	-	-	-	-	-	-	-	-	-
Apr	-	-	-	-	-	-	-	-	-	-
May	-	-	-	-	-	-	-	-	-	-
June	-	-	-	-	-	-	-	-	-	-
Sub-total	0.1682*	0.0000	0.0000	0.1682*	0.0000	0.0000	0.0000	0.0000	0.0000	0.0219*
July	-	-	-	-	-	-	-	-	-	-
Aug	-	-	-	-	-	-	-	-	-	-
Sep	-	-	-	-	-	-	-	-	-	-
Oct	-	-	-	-	-	-	-	-	-	-
Nov	-	-	-	-	-	-	-	-	-	-
Dec	-	-	-	-	-	-	-	-	-	-
Sub-total	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000
Total	0.1682*	0.0000	0.0000	0.1682*	0.0000	0.0000	0.0000	0.0000	0.0000	0.0219*

Assumption:

- i) Density of C&D material = 2.2 tons/m³
- ii) Density of general refuse = 1.6 tons/m³
- iii) Inert C&D material should refer to rock, soil, concrete debris and asphalt generated from site.

* Estimated quantity (To be updated in the next reporting period as per the EPD up-to-date transaction records)

**Appendix K Cumulative statistics on Environmental
Complaints, Notifications of Summons and
Successful Prosecutions**

Statistic Summary of Environmental Complaints

Reporting Period	Environmental Complaints Statistics		
	Frequency	Nature	Follow-up Actions
1 January 2024 – 31 January 2024	0	N/A	N/A
Cumulative	0	N/A	N/A

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Nature	Follow-up Actions
1 January 2024 – 31 January 2024	0	N/A	N/A
Cumulative	0	N/A	N/A

Statistical Summary of Environmental Prosecution





Reporting Period	Environmental Prosecution Statistics		
	Frequency	Nature	Follow-up Actions
1 January 2024 – 31 January 2024	0	N/A	N/A
Cumulative	0	N/A	N/A

Appendix L Complaint Log

Environmental Complaints Log

Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil

Appendix M Observation and Rectification Photos

Date	Environmental Observation(s) / Recommendation(s)	Rectification Photos	Close-out Date / Status
2024 - 1 - 17	<p>Obsevation 1:</p>  <p>1. Haul Road should be sprayed water to enhance dust mitigation measure. (Upper platform)</p>	<p>Action Taken:</p>  <p>1. Haul road was sprayed water to control dust. (Upper platform)</p>	Rectified on 17 January 2024.
	<p>Obsevation 2:</p>  <p>2. Stockpile should be covered by tarpaulin sheet. (Upper platform)</p>	<p>Action Taken:</p>  <p>2. Stockpile was removed. (Upper platform)</p>	Rectified on 17 January 2024.

Document prepared by

Aurecon Hong Kong Limited

Unit 1608, 16/F, Tower B, Manulife Financial Centre,
223 – 231 Wai Yip Street, Kwun Tong, Kowloon
Hong Kong S. A. R.

T +852 3664 6888

F +852 3664 6999

E hongkong@aurecongroup.com

W aurecongroup.com

aurecon

*Bringing ideas
to life*

