

Ref.: CEDKTDS4EM00_0_0372L.24.doc

15 August 2024

AECOM Asia Company Limited
12/F, Grand Central Plaza, Tower 2
138 Shatin Rural Committee Road
Shatin, Hong Kong

By Post and Email

Attention: Ms. Fanny Lau

Dear Madam,

**Re: Contract No. ED/2018/01 – Kai Tak Development
Stage 4 Infrastructure at the Former Runway and South Apron**

Monthly EM&A Report for July 2024

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for July 2024 (Version 1.2) certified by the ET Leader and provided to us via email on 14 August 2024.

Please be advised that we have no further comment on the captioned Monthly EM&A Report in accordance with Condition 3.3 of EP-337/2009 and Condition 3.2 of EP-445/2013/B.

The ET Leader is reminded that it is the ET's responsibility to ensure the report be timely submitted to the Director of Environmental Protection in accordance with the EM&A Manuals and Environmental Permits.

Thank you for your attention. Please do not hesitate to contact the undersigned should you have any queries.

Yours faithfully,
For and on behalf of
Ramboll Hong Kong Limited



Y H Hui
Independent Environmental Checker

c.c. CEDD
Ka Shing
Penta-Ocean

Attn.: Mr. Jason Wong
Attn.: Mr. Chan Pang
Attn.: Mr. Daniel Ho

Fax: 2739 0076
By Email
Fax: 2572 4080

Q:\Projects\CEDKTDS4EM00\02 Proj_Mgt\02 Corr\CEDKTDS4EM00_0_0372L.24.doc

Environmental Monitoring and Audit Report
for
Contract No. ED/2018/01 –
Kai Tak Development – Stage 4 infrastructure at the
former runway and south apron

Contract No.: EDO 15/2018

July 2024

(Version 1.2)

Certified By: _____



(Environmental Team Leader)

Table of Content

Page

EXECUTIVE SUMMARY	1
Breaches of Action and Limit Levels.....	1
Complaint log.....	1
Notifications of summons and successful prosecutions	2
Report changes	2
Key construction works in the reporting month.....	3
Future key issues	3
1. INTRODUCTION	4
Project Background.....	4
Project Organization.....	5
Works Area and Construction Programme.....	5
Construction works undertaken during reporting month.....	6
Submission Status under the Environmental Permits.....	6
2. AIR QUALITY MONITORING	7
Monitoring Requirements.....	7
Monitoring Locations.....	7
Monitoring Parameters, Frequency and Duration	9
Monitoring Equipment	9
Monitoring Methodology and QA/QC Procedure.....	10
Wind Data Monitoring	12
Action and Limit Levels.....	13
Impact Air Quality Monitoring results.....	13
3. NOISE MONITORING	15
Monitoring Requirements.....	15
Monitoring Locations.....	15
Monitoring Parameters, Frequency and Duration	17

	Monitoring Equipment	17
	Monitoring Methodology and QA/QC Procedure	18
	Maintenance and Calibration.....	18
	Action and Limit Levels.....	19
	Impact Noise Monitoring results	19
4.	COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS	21
5.	LANDSCAPE AND VISUAL MONITORING	24
	Results and Observations	24
6.	ENVIRONMENTAL SITE INSPECTION AND AUDIT	25
	Site Inspection	25
	Status of Waste Management	28
	Status of Environmental Licenses, Notification and Permits	28
	Implementation Status of Environmental Mitigation Measures.....	29
	Environmental Complaint and Non-compliance	29
	Notifications of summons and successful prosecutions	29
7.	FUTURE KEY ISSUES	30
	Construction Programme in the coming month.....	30
	Environmental Site Inspection and Monitoring Schedule for next month	31
8.	CONCLUSIONS.....	32

List of Tables

Table I	Non-compliance Record in the Reporting Month
Table II	Summary of complaints in the Reporting Month
Table III	Summary of summons and successful prosecutions in the Reporting Month
Table IV	Summary of future key issues and potential impact in the coming month
Table 1.1	Contact Information of Key Personnel
Table 1.2	Major activities of the Project during reporting month
Table 1.3	Summary of Status of Required Submission of EPs

Table 2.1	Locations of Air Quality Monitoring Stations
Table 2.2	Proposed alternative monitoring locations for AM4(A)
Table 2.3	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.4	Air Quality Monitoring Equipment
Table 2.5	Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring
Table 2.6	Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring
Table 2.7	Summary of 24-hour average TSP Monitoring Data during the reporting month
Table 2.8	Summary of 1-hour average TSP Monitoring Data during the reporting month
Table 3.1	Locations of Noise Monitoring Stations
Table 3.2	Proposed alternative monitoring locations for M11
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Noise Monitoring Equipment
Table 3.5	Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring
Table 3.6	Summary of Noise Monitoring Data during the reporting month
Table 4.1	Comparison of 24-hour average TSP Monitoring Data with EIA predictions
Table 4.2	Comparison of 1-hour average TSP Monitoring Data with EIA predictions
Table 4.3	Comparison of Noise Monitoring Data with EIA predictions
Table 5.1	Summary of observations of Landscape and Visual impact during the reporting month
Table 6.1	Summary of site inspections observations during the reporting month
Table 6.2	Summary of Environmental Licenses, Notifications and Permits
Table 6.3	Summary of complaints in the Reporting Month
Table 6.4	Summary of summons and successful prosecutions in the Reporting Month
Table 7.1	Summary of future key issues and potential impact in the coming month

List of Figure

Figure 1 – Proposed works of Contract No. ED/2018/01

Figure 2 – Proposed Bus Stop And Associated Noise Barrier At Road D3A

Figure 3 – Future Pedestrian Connection Between Landscaped Deck And Private Developments

Figure 4 – Site Layout Plan

Figure 5 – New Opened Road on 31 December 2022

Figure 6 – Air Quality Monitoring Stations

Figure 7 – Proposed Alternative Monitoring Locations for AM4(A)

Figure 8 – Noise Monitoring Stations

Figure 9 – Proposed Alternative Monitoring Locations for M11

List of Appendices

Appendix A – Organization Chart of EM&A Team

Appendix B – Construction Programme

Appendix C – Apply permission for Environmental Monitoring

Appendix D – Environmental monitoring schedules

Appendix E – Photographic records

Appendix F – Calibration certificates, catalogue of air quality monitoring equipment

Appendix G – Weather information

Appendix H – 24-hr TSP monitoring results and graphical presentation

Appendix I – 1-hr TSP monitoring results and graphical presentation

Appendix J – Event and Action Plan for air quality

Appendix K – Calibration certificates, catalogue of noise monitoring equipment

Appendix L – Noise monitoring results and graphical presentation

Appendix M – Event and Action Plan for noise

Appendix N – Event and Action Plan for Landscape and Visual Impact

Appendix O – Waste Flow Table

Appendix P – Environmental Mitigation Implementation Schedule (EMIS)

Appendix Q – Summaries of Environmental Complaint, Warning, Summon and Notification
of Successful Prosecution

EXECUTIVE SUMMARY

This is the 55th Monthly Environmental Monitoring & Audit (EM&A) report which summaries the findings of the EM&A Programme during the reporting period from 1 to 31 July 2024.

Breaches of Action and Limit Levels

- 1) 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 2) 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 3) Construction noise monitoring was conducted as scheduled in the reporting month. No Action Level and Limit Level exceedance was recorded in the reporting month.
- 4) Summary of the non-compliance in the reporting month for the Project is tabulated in Table I.

Table I Non-compliance Record in the Reporting Month

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
1-hr TSP	0	0	N/A
24-hr TSP	0	0	N/A
Construction noise	0	0	N/A

Complaint log

- 5) No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table II.

Table II Summary of complaints in the Reporting Month

Date of complaint received	Description of complaint	Investigation / Recommendations / Action taken	Close-out date / Status
NA	NA	NA	NA

Date of complaint received	Description of complaint	Investigation / Recommendations / Action taken	Close-out date / Status

Notifications of summons and successful prosecutions

- 6) No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table III.

Table III Summary of summons and successful prosecutions in the Reporting Month

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action take	Close-out date / Status
No notification of summons and successful prosecutions were received in the reporting month.	NA	NA	NA	NA

Report changes

- 7) There was no reporting change in the reporting month.

Key construction works in the reporting month

8) Major construction activities undertake during the reporting month included:

- Installation of steel roof structure at Observation Deck
- Granolithic finishing works of Harbour Steps
- Construction of thrust block, wash-out chamber, manhole for drainage works & draw pit for cable works.
- Flow rate test of DCS Intake Box Culvert
- Construction of Event Deck no. 2
- Installation of internal partition of Temporary Management Office
- Installation of steel roof structure & internal partition of Toilet cum and Changing Room
- Installation of drainage near Pumping Stations
- Finishing work in Pumping Stations
- Erection of cladding of Feature Shelter, planter kerb at Elevated Landscape Deck

Future key issues

9) The future key issues and potential impact in the coming month are given in Table IV.

Table IV Summary of future key issues and potential impact in the coming month

Future key issues in the coming month	Potential impact
Construction of Event Deck nos. 1 & 3	Noise and Air Quality, Chemical and Waste Management
Construction of footings of Honed Concrete. Installation of precast units of Honed Concrete.	Noise, Air and Water Quality
Construction of thrust block, wash-out chamber, manhole for drainage works & draw pit for cable works	Noise and Air Quality, Chemical and Waste Management
Installation of fire main pipe, irrigation pipe, cleansing pipe	Noise and Air Quality, Chemical and Waste Management
Installation of glass balustrade	Noise and Air Quality, Chemical and Waste Management
Installation of internal partition of Temporary Management Office	Noise, Air and Water Quality
Installation of E&M equipment and finishing work in Pumping Stations	Noise and Air Quality, Chemical and Waste Management
Erection of cladding of Feature Shelter & Rain Shelter, planter kerb at Elevated Landscape Deck	Noise and Air Quality, Chemical and Waste Management
Planting work at Elevated Landscape Deck	Noise and Air Quality, Chemical and Waste Management

1. INTRODUCTION

Project Background

- 1.1 The Kai Tak Development (KTD) is located in the south-eastern part of Kowloon Peninsula of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling.
- 1.2 Contract No. ED/2018/01 - Kai Tak Development – stage 4 infrastructure at the former runway and south apron (The Project), comprises mainly the design and construction of a dual two-lane Road D3 (Metro Park Section), a single 2-lane Road L12d, a salt water pumping station, a sewage pumping station, landscaped deck and promenade above and adjoining Road D3 (Metro Park Section) respectively, some remaining road works at Road L14, noise barrier at Road D3A, and other associated works at the former runway and south apron. The proposed works are shown in Figure 1 and Figure 2. During the course of the Contract No. ED/2018/01, there may be modification of noise barriers in association with the construction of footbridges connecting to the landscaped deck of Road D3A by developers of adjacent lands (Figure 3). The proposed works and site boundary are shown in Figure 4.
- 1.3 The new road connecting Shing Fung Road & Shing Kai Road has been open for public vehicles since 31 December 2022. Detailed location referring to Figure 5.
- 1.4 Civil Engineering and Development Department (CEDD) had completed an Environmental Impact Assessment (EIA) and is the Permit Holder.
- 1.5 The construction work under ED/2018/01 comprises the EM&A Manuals (EIA Register Nos. AEIAR-130/2009 for Kai Tak Development and EIA Register Nos. AEIAR-170/2013 for Roads D3A and D4A) and Environmental Permit (EP) Nos. EP-337/2009 and Variation to the EP (VEP) No. EP-445/2013/B.
- 1.6 Air quality and noise monitoring has been proposed in the EM&A Manual with EIA Register Nos. AEIAR-130/2009 for Kai Tak Development while no air quality and noise monitoring are proposed in EM&A Manual with EIA Register Nos. AEIAR-170/2013 for Roads D3A and D4A.

Project Organization

1.7 The project organization chart and with respect to the EM&A programme is shown in Appendix A. Information of key personnel contact names and telephone numbers are summarized in Table 1.1.

Table 1.1 Contact Information of Key Personnel

Party	Role	Contact Person	Position	Phone No.	Fax No.
Civil Engineering and Development Department (CEDD)	Project Proponent	Mr. Jason Wong	Senior Engineer	3579 2453	2739 0076
		Ms. Chan Ka Yan	Engineer	3579 2458	2739 0076
AECOM Asia Co. Ltd. (AECOM)	Supervisor (act as Engineers' Representative (ER) listed in EM&A Manual)	Ms. Fanny Lau	CRE	3911 4201	3911 4288
Ramboll Hong Kong Limited (Ramboll)	Independent Environmental Checker (IEC)	Mr. Y H Hui	IEC	3465 2850	3465 2899
Ka Shing Management Consultant Limited (Ka Shing)	Environmental Team (ET)	Mr. Chan Pang	ET Leader	6082 2973	2120 7752
Penta-Ocean Construction Co., Ltd. (Penta-Ocean)	Contractor	Mr. Tony Tang	Environmental Officer	9433 2628	3465 8898

Works Area and Construction Programme

1.8 The construction works commenced on 20 January 2020. The construction programme of the Project is given in Appendix B.

Construction works undertaken during reporting month

1.9 Major construction works of the Project in the reporting month are summarized in Table 1.2:

Table 1.2 Major activities of the Project during reporting month

Installation of steel roof structure at Observation Deck	Granolithic finishing works of Harbour Steps
Construction of thrust block, wash-out chamber, manhole for drainage works & draw pit for cable works	Flow rate test of DCS Intake Box Culvert
Construction of Event Deck no. 2	Installation of internal partition of Temporary Management Office
Installation of steel roof structure & internal partition of Toilet cum and Changing Room	Installation of drainage near Pumping Stations
Finishing work in Pumping Stations	Erection of cladding of Feature Shelter, planter kerb at Elevated Landscape Deck

Submission Status under the Environmental Permits

1.10 The status of required submission under Environmental Permit (EP) conditions under EP-337/2009 and Variation to the EP (VEP) No. EP-445/2013/B are summarized in Table 1.3.

Table 1.3 Summary of Status of Required Submission of EPs

EP Condition EP-337/2009	EP Condition EP-445/2013/B	Submission	Submission Date
Condition 1.11	Condition 1.12	Notification of Commencement Date of Construction of the Project	6 Jan 2020
Condition 2.3	Condition 2.3	Management Organization of Main Construction Companies	9 Sep 2019
Condition 2.3	Condition 2.3	Updated Management Organization of Main Construction Companies	17 Aug 2021
Condition 2.4	Condition 2.4	Design Drawings	6 Jan 2020
Condition 2.11	Condition 2.5	Landscape Mitigation Plans	13 Nov 2020
Condition 2.1	Condition 2.5	Landscape Mitigation Plans (Revision 2)	18 May 2021
NA	Condition 2.9	Detailed Design Plan of Traffic Noise Mitigation Measures	9 Dec 2022
Condition 3.2	NA	Baseline Monitoring Report	2 Jan 2020
Condition 3.2	NA	Revised Baseline Monitoring Report	28 Mar 2020
Condition 3.3	Condition 3.2	Monthly EM&A Report (June 2024)	12 July 2024

2. AIR QUALITY MONITORING

Monitoring Requirements

2.1 In accordance with EM&A Manuals (EIA Register Nos. AEIAR-130/2009), impact air quality monitoring shall be carried out during the construction phase of the Project. For regular impact monitoring, a sampling frequency of at least once in every six days will be strictly observed at all of the monitoring stations for 24-hour TSP. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days will be undertaken when the highest dust impact occurs.

Monitoring Locations

2.2 Three designated monitoring stations were selected for air quality monitoring programme. Impact air quality monitoring was conducted at three air quality monitoring stations in the reporting month. Table 2.1 describes the air quality monitoring locations, which are also depicted in Figure 6.

Table 2.1 Locations of Air Quality Monitoring Stations

Air Quality Monitoring Locations for the Project	Location of Measurement
AM3 - Sky Tower	Podium floor near T7
AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop	Ground
AM7 – Hong Kong Children's Hospital	Rooftop

2.3 Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A) while 1-hr TSP monitoring at AM4(A) were conducted on the ground floor with orienting to the Project site.

2.4 ET approached the potential sensitive receivers for monitoring station relocation since May 2022. ET conducted site visit in nearby area and found that there was no property management company in most of the nearby premises and could not approach the residents regarding the environmental monitoring. No permission can be applied for environmental monitoring.

2.5 For those premises have property management company, ET sent the proposal to owner /

property management company and explained the purpose of environmental monitoring (refer to Appendix C – Apply permission for Environmental Monitoring). Figure 7 shows the proposed alternative monitoring locations. No permission of setup and entry is received until the reporting month.

2.6 Summary of the status of for proposed alternative monitoring locations for AM4(A) are given in Table 2.2.

Table 2.2 Proposed alternative monitoring locations for AM4(A)

Proposed alternative monitoring locations for M11	Status upto reporting month
A1 - The Lok Sin Tong Modular Social Housing Scheme	Rejected application on 13 Oct 2022
A2 - Freder Centre	No reply from building management office
A3 - New Port Centre	No reply from building management office
A4 - 112 - 138 To Kwa Wan Road	No property management company and could not apply the permission.
A5 - 2 - 26 Hok Ling Street	No property management company and could not apply the permission.
A6 - 1 - 27 Hok Ling Street	No property management company and could not apply the permission.
A7 - 2 - 28 Tsun Fat Street	No property management company and could not apply the permission.
A8 - 1 - 27 Tsun Fat Street	No property management company and could not apply the permission.
A9 - 2 - 28 Yin On Street	No property management company and could not apply the permission.
A10 - 1 - 27 Yin On Street	No property management company and could not apply the permission.
A11 - 2 - 28 Shim Luen Street	No property management company and could not apply the permission.
A12 - 1 - 27 Shim Luen Street	No property management company and could not apply the permission.
A13 - 2 - 28 Hung Wan Street	No property management company and could not apply the permission.
A14 - 1 - 27 Hung Wan Street	No property management company and could not apply the permission.
A15 - 2 - 28 Pang Ching Street	No property management company and could not apply the permission.
A16 - 1 - 27 Pang Ching Street	No property management company and could not apply the permission.
A17 - 2 - 28 Ying Yeung Street	No property management company and could not apply the permission.
A18 - 1 - 27 Ying Yeung Street	No property management company and could not apply the permission.
A19 - 2 - 28 Lun Cheung Street	No property management company and could not apply the permission.
A20 - 1 - 27 Lun Cheung Street	No property management company and could

Proposed alternative monitoring locations for M11	Status upto reporting month
	not apply the permission.
A21 - 2 - 28 Luk Ming Street	No property management company and could not apply the permission.
A22 - 1 - 27 Luk Ming Street	No property management company and could not apply the permission.
A23 - 2 - 28 Fung Yi Street	No property management company and could not apply the permission.

2.7 No update for the approval of monitoring relocation in the reporting month and ET will resume the impact monitoring once the alternative monitoring location for AM4(A) are confirmed.

Monitoring Parameters, Frequency and Duration

2.8 The air quality monitoring locations and monitoring frequency are listed in Table 2.3.

Table 2.3 Air Quality Monitoring Parameters, Frequency and Duration

Air Monitoring Station	Location for Measurement	Parameter	Duration	Frequency
AM3 - Sky Tower	Podium floor near T7	- 24-hour average TSP - 1-hour average TSP	- 24 hours - 1 hour	- Once every 6 days - Three times every 6 days
AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop	Ground			
AM7 - Hong Kong Children's Hospital	Rooftop			

2.9 The monitoring schedule for reporting month and next month is presented in Appendix D

2.10 Photographic records of the impact monitoring setup are shown in Appendix E.

Monitoring Equipment

2.11 24-hour average TSP and 1-hour average TSP levels were measured for impact monitoring. 24-hour average TSP levels were measured by the High Volume Samplers (HVS) and 1-hour average TSP levels were measured by direct reading method to indicate short-term impacts. Wind data monitoring equipment was set up at conspicuous locations for logging wind speed

and wind direction near to the dust monitoring locations. Table 2.4 summarizes the equipment to be used in the air quality monitoring.

Table 2.4 Air Quality Monitoring Equipment

Equipment	Model	Quantity
HVS Sampler	TE-5170 X c/w of TSP sampling inlet	2
Calibrator	TISCH TE-5025A	1
1-hour TSP Dust Meter	TSI Model AM510 SidePak Personal Aerosol Monitor	2
Wind Anemometer	Davis Vantage Pro2 Weather Station	1

2.12 High volume samplers (HVS) (TE-5170 X c/w of TSP sampling inlet) comprising with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

2.13 Calibration certificates, catalogue of equipment are given in Appendix F.

Monitoring Methodology and QA/QC Procedure

24-hour TSP Monitoring

Operating/Analytical Procedures

2.14 Setup criteria of HVS are shown as follows:

- A horizontal platform with appropriate support to secure the samplers against gusty wind was provided.
- No two samplers were placed less than 2m apart.
- The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2m of separation from walls, parapets and penthouses was set for the rooftop samples.
- A minimum of 2m separation from any supporting structure, measured horizontally was set.
- No furnaces or incineration flues was nearby.
- Airflow around the sampler was unrestricted.
- Any wire fence and gate, to protect the samplers, was not caused any obstruction during

monitoring.

- Permission were obtained to setup the samplers and to obtain access to the monitoring stations.
- A secured supply of electricity was provided to operate the samplers.

2.15 Prior to the commencement of the dust sampling, the flow rate of the HVS was properly set (between 1.1 m³/min. and 1.7 m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.

2.16 For TSP sampling, Glass Fiber Filter Media 8" x 10" have a collection efficiency of > 99 % for particles of 0.3 µm diameter were used.

2.17 The power supply was checked to ensure the sampler worked properly and then placed any filter media at the designated air monitoring station.

2.18 The filter holding frame was removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.

2.19 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure was sufficient to avoid air leakage at the edges.

2.20 The shelter lid was closed and secured with the aluminium strip.

2.21 The timer was programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).

2.22 After sampling, the filter was removed from the HVS and put into a clean and labeled seal plastic bag to avoid cross contamination. The elapsed time was also be recorded. The sampled filters were sent to the HOKLAS accredited or other internationally accredited laboratory for weighting.

Maintenance/Calibration

2.23 The following maintenance/calibration are required for the HVS:

- The HVS and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
- High volume samplers were calibrated with at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

1-hour TSP Monitoring

Measurement Procedures

2.24 The measurement procedures of the 1-hour TSP were conducted in accordance with the Manufacturer's Instruction Manual as follows:

- Set up the dust meter on a tripod at 1.2m level.
- Turned on the dust meter and check the battery, if too low, change new ones. Pointed the meter to the source area or the planned measurement area.
- The zero calibration of the instrument was conducted before and after each sampling.
- TSP levels were recorded for 1-hour with 5-minute data logging interval.
- Recorded down the general meteorological conditions, Test ID no., start/end time, spot check reading at each sampling location for data processing.
- Recorded any activities that may generate dust during measurement period.

Maintenance/Calibration

2.25 The following maintenance/calibration are required for the direct dust meters:

- To validity the accuracy of dust meter, compare the results measured by dust meter and HVS by direct reading method every 12 months throughout all stages of the air quality monitoring.

Wind Data Monitoring

2.26 Wind Anemometer was installed at the roof-top of AM7 - Hong Kong Children's Hospital with 10m above ground and clear of constructions or turbulence caused by the buildings.

2.27 The wind data was captured by a data logger and the data was downloaded at least once per month for analysis.

2.28 The wind data monitoring equipment will be re-calibrated at least once every six months.

2.29 Wind direction is divided into 16 sectors of 22.5 degrees each.

2.30 Details of weather information during the monitoring period are shown in Appendix G.

Action and Limit Levels

2.31 The Action and Limit Levels of 24-hour average TSP and 1-hour average TSP are summarized in Table 2.5 and Table 2.6 respectively.

Table 2.5 Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
24-hour average TSP	AM3	182	260
	AM4(A)	187	260
	AM7	181	260

Table 2.6 Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hour average TSP	AM3	297	500
	AM4(A)	326	500
	AM7	315	500

Impact Air Quality Monitoring results

2.32 Impact monitoring results for 24-hour average TSP and 1-hour average TSP levels at the designed air quality monitoring stations are summarized in Table 2.7 and Table 2.8 respectively.

2.33 Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A) while 1-hr TSP monitoring at AM4(A) were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for AM4(A) is confirmed.

Table 2.7 Summary of 24-hour average TSP Monitoring Data during the reporting month

Air Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM3	55	32 – 78	182	260
AM4(A)	/	/ – /	187	260
AM7	42	24 – 62	181	260

Table 2.8 Summary of 1-hour average TSP Monitoring Data during the reporting month

Air Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM3	53	31 – 77	297	500
AM4(A)	60	34 – 88	326	500
AM7	45	33 – 60	315	500

2.34 There was no Action and Limit Level exceedance of 24-hour average TSP and 1-hour average TSP levels recorded during the reporting month.

2.35 Graphical presentation and detailed monitoring results of 24-hour average TSP and 1-hour average TSP levels are shown in Appendix H and Appendix I respectively.

2.36 The Event and Action Plan is provided in Appendix J.

2.37 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

3. NOISE MONITORING

Monitoring Requirements

- 3.1 In accordance with EM&A Manuals (EIA Register Nos. AEIAR-130/2009), impact noise monitoring shall be carried out during the construction phase of the Project.
- 3.2 Regular monitoring, $L_{Aeq, 30\text{-minute}}$, for each station will be on a weekly basis and conduct one set of measurements between 0700 – 1900 on normal weekdays.
- 3.3 If construction works are extended to include works during 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring will be carried out during the respective restricted hours periods.

Monitoring Locations

- 3.4 Two designated monitoring stations were selected for noise monitoring programme. Impact noise monitoring was conducted at two noise monitoring stations in the reporting month. Table 3.1 describes the noise monitoring locations, which are also depicted in Figure 8.

Table 3.1 Locations of Noise Monitoring Stations

Noise Monitoring Locations for the Project	Location of Measurement
M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop	Ground (Façade)
M12 - Hong Kong Children's Hospital	Rooftop (Façade)

- 3.5 Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022.
- 3.6 ET approached the potential sensitive receivers for monitoring station relocation since May 2022. ET conducted site visit in nearby area and found that there was no property management company in most of the nearby premises and could not approach the residents regarding the environmental monitoring. No permission can be applied for environmental monitoring.

3.7 For those premises have property management company, ET sent the proposal to owner / property management company and explained the purpose of environmental monitoring (refer to Appendix C – Apply permission for Environmental Monitoring). Figure 9 shows the proposed alternative monitoring locations. No permission of setup and entry is received until the reporting month.

3.8 Summary of the status of for proposed alternative monitoring locations for M11 are given in Table 3.2.

Table 3.2 Proposed alternative monitoring locations for M11

Proposed alternative monitoring locations for M11	Status upto reporting month
A1 - The Lok Sin Tong Modular Social Housing Scheme	Rejected application on 13 Oct 2022
A2 - Freder Centre	No reply from building management office
A3 - New Port Centre	No reply from building management office
A4 - 112 - 138 To Kwa Wan Road	No property management company and could not apply the permission.
A5 - 2 - 26 Hok Ling Street	No property management company and could not apply the permission.
A6 - 1 - 27 Hok Ling Street	No property management company and could not apply the permission.
A7 - 2 - 28 Tsun Fat Street	No property management company and could not apply the permission.
A8 - 1 - 27 Tsun Fat Street	No property management company and could not apply the permission.
A9 - 2 - 28 Yin On Street	No property management company and could not apply the permission.
A10 - 1 - 27 Yin On Street	No property management company and could not apply the permission.
A11 - 2 - 28 Shim Luen Street	No property management company and could not apply the permission.
A12 - 1 - 27 Shim Luen Street	No property management company and could not apply the permission.
A13 - 2 - 28 Hung Wan Street	No property management company and could not apply the permission.
A14 - 1 - 27 Hung Wan Street	No property management company and could not apply the permission.
A15 - 2 - 28 Pang Ching Street	No property management company and could not apply the permission.
A16 - 1 - 27 Pang Ching Street	No property management company and could not apply the permission.
A17 - 2 - 28 Ying Yeung Street	No property management company and could not apply the permission.
A18 - 1 - 27 Ying Yeung Street	No property management company and could not apply the permission.
A19 - 2 - 28 Lun Cheung Street	No property management company and could

Proposed alternative monitoring locations for M11	Status upto reporting month
	not apply the permission.
A20 - 1 - 27 Lun Cheung Street	No property management company and could not apply the permission.
A21 - 2 - 28 Luk Ming Street	No property management company and could not apply the permission.
A22 - 1 - 27 Luk Ming Street	No property management company and could not apply the permission.
A23 - 2 - 28 Fung Yi Street	No property management company and could not apply the permission.

3.9 No update for the approval of monitoring relocation in the reporting month and ET will resume the impact monitoring once the alternative monitoring location for M11 are confirmed.

Monitoring Parameters, Frequency and Duration

3.10 The noise monitoring locations and monitoring frequency are listed in Table 3.3.

Table 3.3 Noise Monitoring Parameters, Frequency and Duration

Noise Monitoring Station	Location for Measurement	Parameter	Frequency and Duration
M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop*	Ground (Façade)	L_{Aeq} , L_{A10} and L_{A90}	30 - minutes measurement at each monitoring station between 0700 – 1900 hrs on normal weekdays (Monday to Saturday) at frequency of once per week.
M12 - Hong Kong Children's Hospital	Rooftop (Façade)		

* Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022.

3.11 The monitoring schedule for reporting month and next month is presented in Appendix D.

3.12 Photographic records of the monitoring setup are shown in Appendix E.

Monitoring Equipment

3.13 As referred to in the Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO), sound level meters in compliance with the IEC 61672-1 (Type 1) standard [this

standard replaced the International Electrotechnical Commission Publications 60651:1979 (Type 1) and 60804:1985 (Type 1)] were used for noise monitoring. Table 3.4 summarizes the equipment to be used in the noise monitoring.

Table 3.4 Noise Monitoring Equipment

Equipment	Model	Quantity
Sound Level Meter	RION NL52	2
Sound Level Calibrator	RION NC 74	1
Sound Level Calibrator	RION NC 75	1
Air Flowmeter	TSI TA440 Air Velocity	1

3.14 Calibration certificates, catalogue of equipment are given in Appendix K.

Monitoring Methodology and QA/QC Procedure

3.15 The noise level measurement was conducted at 1m from the exterior of the nearby noise sensitive receivers building façade and at 1.2m above the ground and facing to the source area or the planned measurement area.

3.16 No noise measurement was conducted in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. Air flow was measured by air flow meter.

3.17 Turned on the sound level meter and check the battery, if too low, change new ones.

3.18 Calibration was conducted immediately prior to and after each noise measurement, the accuracy of the sound level meters was checked by using sound calibrator generating 1,000 Hz with 94dB. Measurement data was found to be valid only if the calibration levels from before and after the noise measurement agreed to within 1.0 dB.

3.19 Noise level was recorded.

3.20 Recorded any activities that may generate noise during measurement period.

Maintenance and Calibration

3.21 The microphone head of the sound level meter and calibrator was cleaned with a soft cloth at quarterly intervals.

3.22 The sound level meter and sound calibrator were calibrated annually.

3.23 Calibration for sound level meter was conducted immediately prior to and following each noise measurement by using sound calibrator generating a known sound pressure level at a known frequency (1,000 Hz with 94dB). Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

Action and Limit Levels

3.24 The Baseline Noise Levels and Action and Limit Levels for construction noise is presented in Table 3.5.

Table 3.5 Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring

Time Period	Noise Monitoring Station	Baseline Noise Levels, dB (A)	Action Level	Limit Level [^]
0700 – 1900 on normal weekdays	M11	68.3	When one documented complaint is received.	75 dB(A)
	M12	61.9		

Note: ^ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Impact Noise Monitoring results

3.25 Impact noise monitoring results at the designed noise monitoring stations are summarized in Table 3.6 respectively.

3.26 Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 30-min noise monitoring at M11 were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for M11 is confirmed.

Table 3.6 Summary of Noise Monitoring Data during the reporting month

Noise Monitoring Station	Measured $L_{Aeq, 30\text{-min}}$, Average, dB(A)	Measured $L_{Aeq, 30\text{-min}}$, Range, dB(A)	Action Level	Limit Level ^
M11	72.8	71.6 – 73.6	When one documented complaint is received	75 dB(A)
M12	63.3	62.4 – 64.7		

Note: ^ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

3.27 There were no Action Level exceedance of noise monitoring and Limit Level exceedance of $L_{Aeq, 30\text{min}}$ recorded during the reporting month.

3.28 Graphical presentation and detailed monitoring results are shown in Appendix L.

3.29 The Event and Action Plan is provided in Appendix J.

3.30 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

4. COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS

4.1 The environmental impacts predictions were given in Agreement No. CE 35/2006(CE) Kai Tak Development Engineering Study cum Design and Construction of Advance Works - Investigation, Design and Construction - Kai Tak Development Environmental Impact Assessment Report, EIA Register Nos. AEIAR-130/2009 for Kai Tak Development (The EIA Report). The EM&A data was compared with the EIA predictions as summarized in Table 4.1 to Table 4.3.

Table 4.1 Comparison of 24-hour average TSP Monitoring Data with EIA predictions

Air Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 24-hour average TSP concentration		Measured 24-hr average TSP in Reporting Month (July 2024) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM3 - Sky Tower	A40 [^]	106	138	32 – 78
AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop*	A43 [^]	123	195	/ – /
AM7 – Hong Kong Children's Hospital	PA60	NA	NA	24 – 62

Note:

[^] Prediction results are given in the Table 3.13 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

* Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A) because of the assess limitation in the reporting month.

Table 4.2 Comparison of 1-hour average TSP Monitoring Data with EIA predictions

Air Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 1-hour average TSP concentration		Measured 1-hr average TSP in Reporting Month (July 2024) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM3 - Sky Tower	A40	217 [^]	247 [^]	31 – 77
AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop*	A43	283 [^]	409 [^]	34 – 88
AM7 – Hong Kong Children's Hospital	PA60	NA	NA	33 – 60

Note:

^ Prediction results are given in the Table 3.13 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

* Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 1-hour TSP monitoring was conducted on the ground floor outside AM4(A) with facing to the Project Site because of the access limitation in the reporting month.

Table 4.3 Comparison of Noise Monitoring Data with EIA predictions

Noise Monitoring Station	NSR No. in EIA report	Predicted Mitigated Construction Noise Levels during Normal Daytime Working Hour L _{Aeq} , 30min, dB(A)	Measured Noise Level in Reporting Month (July 2024) L _{Aeq} , 30min, dB(A)
M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop*	N18	50 – 76*	71.6 – 73.6
M12 - Hong Kong Children's Hospital	PN83, PN84, PN84A	NA	62.4 – 64.7

Note:

* Prediction results are given in the Table 3.20 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

*Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. Construction noise monitoring was conducted on the ground floor outside M11 with facing to the Project Site because of the access limitation in the reporting month.

4.2 24-hr TSP monitoring result at AM3 were recorded lower than the prediction in the EIA Report. Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A) because of the assess limitation in the reporting month. Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

4.3 No prediction in the EIA Report for 24-hour TSP monitoring results at AM7.

4.4 1-hour TSP monitoring results at AM3 and AM4(A) were recorded lower than the prediction in the EIA Report. Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 1-hour TSP monitoring was conducted on the ground floor outside AM4(A) with facing to the Project Site because of the access limitation in the reporting month. Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

4.5 No prediction in the EIA Report for 1-hour TSP monitoring results at AM7.

4.6 Noise monitoring results at M11 were recorded lower than the prediction in the EIA Report.

Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. Construction noise monitoring was conducted on the ground floor outside M11 with facing to the Project Site because of the access limitation in the reporting month. Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

4.7 No prediction in the EIA Report for noise monitoring results at M12.

5. LANDSCAPE AND VISUAL MONITORING

5.1 In accordance with EM&A Manuals (EIA Register Nos. AEIAR-130/2009 and AEIAR-170/2013), Landscape and Visual Monitoring shall be carried out during the construction phase of the Project. Regular impact monitoring will be conducted at least once per week.

Results and Observations

5.2 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.

5.3 Site inspections were conducted on 4, 9, 18 and 25 July 2024 in the reporting month.

5.4 The summaries of site audits are attached in Table 5.1.

Table 5.1 Summary of observations of Landscape and Visual impact during the reporting month

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
04 July 2024	No	NA	NA
09 July 2024	No	NA	NA
18 July 2024	No	NA	NA
25 July 2024	No	NA	NA

5.5 No non-compliance of the landscape and visual impact was recorded in the reporting month.

5.6 Should non-compliance of the landscape and visual impact occur, action in accordance with the action plan presented in Appendix N shall be performed.

6. ENVIRONMENTAL SITE INSPECTION AND AUDIT


Site Inspection

6.1 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.


6.2 Site inspections were conducted on 4, 9, 18 and 25 July 2024 in the reporting month.

6.3 The summaries of site audits are attached in Table 6.1.

Table 6.1 Summary of site inspections observations during the reporting month

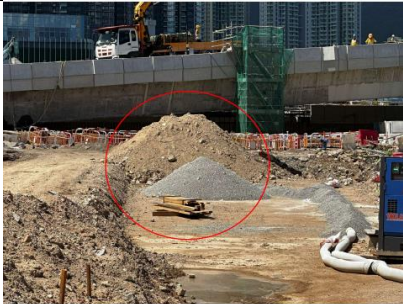Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
04 July 2024	No	NA	NA
09 July 2024	 Observation: Stockpiles should be fully covered by impermeable sheeting to reduce dust emission in area1.	 Action Taken: Stockpiles have been removed to reduce dust emission in area1.	Closed-out on 18 July 2024
			Closed-out on 18 July 2024

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
	 Observation: Water spring on haul should be enhanced to reduce dust emission in area 2 and area 5.	 Action Taken: Water spring on haul have been enhanced to reduce dust emission in area 2 and area 5.	
	 Observation: The construction machine found dark exhaust emissions at the harbour step.	 Action Taken: The construction machine that emitted dark smoke was deactivated at the harbour step.	Closed-out on 18 July 2024
18 July 2024	 Observation: The accumulation waste should be removed regularly at pumping station.	 Action Taken: The accumulation waste was removed regularly at pumping station.	Closed-out on 25 July 2024
			Closed-out on 25 July 2024

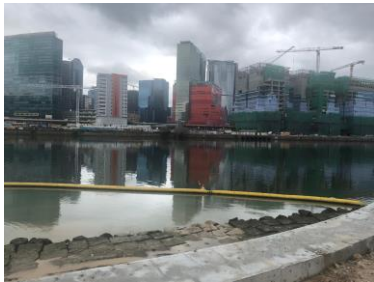Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
	Observation: The stagnant water should be removed regularly at pumping station.	Action Taken: The stagnant water was removed regularly at pumping station.	
	 Observation: The sediment tank should be maintained regularly near the harbour step.	 Action Taken: The sediment tank has been maintained regularly near the harbour step.	Closed-out on 25 July 2024
	 Observation: The control of site runoff from entering the nearby water environment should be implemented and maintained regularly to minimize water quality impact.	 Action Taken: The control of site runoff from entering the nearby water environment have been implemented and maintained regularly to minimize water quality impact.	Closed-out on 25 July 2024
25 July 2024	 Observation:	 Action Taken:	Closed-out on 01 August 2024

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
	The silt curtain should be reinstalled properly at the Harbour steps.	The silt curtain has been reinstalled properly at the Harbour steps.	
	 Observation: The main haul road at the Park 1 should be sprayed with water.	 Action Taken: The main haul road at the Park have been sprayed with water.	Closed-out on 01 August 2024

Status of Waste Management

- 6.4 The amount of wastes generated by the major site activities of the work contracts within the Project during the reporting month is shown in Appendix O.
- 6.5 The Contractor was registered as a chemical waste producer for the Project. The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

Status of Environmental Licenses, Notification and Permits

- 6.6 A summary of the relevant permits, licenses and/or notifications on environmental protection for the Project is shown in Table 6.2.

Table 6.2 Summary of Environmental Licenses, Notifications and Permits

Environmental Licenses, Notifications and Permits	Ref. No.	Valid Form	Valid Till
Environmental Permit under EIAO	EP-337/2009	23 Apr 2009	N/A
	EP-445/2013/B	3 May 2022	N/A
Construction Dust Notification under APCO	445956	6 Jun 2019	N/A
Wastewater Discharge License under WPCO	WT00034610-2019	26 Sep 2019	30 Sep 2024
Waste Disposal Billing Account	7034450	28 Jun 2019	N/A

Environmental Licenses, Notifications and Permits	Ref. No.	Valid Form	Valid Till
Registration as a Chemical Waste Producer	5218-286-P3182-03	18 Jul 2019	N/A
Construction Noise Permit	GW-RE0525-24	30 Apr 2024	29 Oct 2024
	GW-RE0526-24	30 Apr 2024	29 Oct 2024
	GW-RE0063-24	30 Jan2024	28 Jul 2024
	GW-RE0064-24	05 Feb 2024	04 Jul 2024
	GW-RE0082-24	14 Feb 2024	13 Aug 2024
	GW-RE0445-24	21 Apr 2024	20 Oct 2024
	GW-RE0570-24	10 May 2024	09 Nov 2024
	GW-RE0787-24	05 Jul 2024	04 Jan 2025

Implementation Status of Environmental Mitigation Measures

6.7 The Contractor has implemented environmental mitigation measures and requires as stated in the EIA reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting month is summarized in Appendix P.

6.8 In response to the site audit findings, the Contractor carried out corrective actions with summary given in Appendix P.

Environmental Complaint and Non-compliance

6.9 No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table 6.3.

Table 6.3 Summary of complaints in the Reporting Month

Date of complaint received	Description of complaint	Investigation / Recommendations / Action taken	Close-out date / Status
NA	NA	NA	NA

6.10 Complaint log and Complaint Investigation report are shown in Appendix Q.

Notifications of summons and successful prosecutions

6.11 No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table

6.4.

Table 6.4 Summary of summons and successful prosecutions in the Reporting Month

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
No notification of summons and successful prosecutions were received in the reporting month.	NA	NA	NA	NA

6.12 The summaries of cumulative environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in Appendix Q.

7. FUTURE KEY ISSUES

Construction Programme in the coming month

7.1 The major construction activities and potential impacts in the next reporting month as follow:

Table 7.1 Summary of future key issues and potential impact in the coming month

Future key issues in the coming month	Potential impact
Construction of Event Deck nos. 1 & 3	Noise and Air Quality, Chemical and Waste Management
Construction of footings of Honed Concrete. Installation of precast units of Honed Concrete.	Noise, Air and Water Quality
Construction of thrust block, wash-out chamber, manhole for drainage works & draw pit for cable works	Noise and Air Quality, Chemical and Waste Management
Installation of fire main pipe, irrigation pipe, cleansing pipe.	Noise and Air Quality, Chemical and Waste Management
Installation of glass balustrade	Noise and Air Quality, Chemical and Waste Management
Installation of internal partition of Temporary Management Office	Noise, Air and Water Quality
Installation of steel roof structure & internal partition of Toilet cum and Changing Room	Noise and Air Quality, Chemical and Waste Management
Installation of E&M equipment and finishing work in Pumping	Noise and Air Quality, Chemical

Future key issues in the coming month	Potential impact
Stations	and Waste Management
Erection of cladding of Feature Shelter & Rain Shelter, planter kerb at Elevated Landscape Deck	Noise and Air Quality, Chemical and Waste Management
Planting work at Elevated Landscape Deck	Noise, Air and Water Quality

7.2 The mitigation measures for environmental impact including Air Quality, Construction Noise, Water Quality, Chemical and Waste Management, Landscape and Visual shall be implemented:

- Sufficient watering of the works site with the active dust emitting activities,
- Limitation of the speed for vehicles on unpaved site roads,
- Properly cover the stockpiles,
- Good maintenance to the plant and equipment,
- Use of quieter plant and Quality Powered Mechanical Equipment (QPME),
- Provide movable noise barriers,
- Appropriate desilting/ sedimentation devices provided on site for treatment before discharge,
- Well maintain the drainage system to prevent the spillage of wastewater during heavy rainfall,
- Onsite waste sorting and implementation of trip ticket system,
- Good management and control on construction waste reduction,
- Erection of decorative screen hoarding,
- Strictly following the Environmental Permits and Licenses, and
- Provide sufficient mitigation measures as recommended in Approved EIA Reports.

Environmental Site Inspection and Monitoring Schedule for next month

7.3 The tentative schedule for weekly site inspection and air quality and noise monitoring in the next month is provided in Appendix D.

8. CONCLUSIONS

- 8.1 Environmental monitoring works were performed in the reporting month and all monitoring results were checked and reviewed.
- 8.2 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 1-hour TSP monitoring was conducted on the ground floor outside AM4(A) with facing to the Project Site because of the access limitation in the reporting month.
- 8.3 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-hour TSP monitoring was conducted at AM4(A) because of the access limitation in the reporting month.
- 8.4 Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. Impact monitoring was conducted on the ground floor outside M11 with facing to the Project Site because of the access limitation in the reporting month.
- 8.5 No complaint was received in the reporting month.
- 8.6 No notification of summons and successful prosecutions was received in the reporting month.

Figure

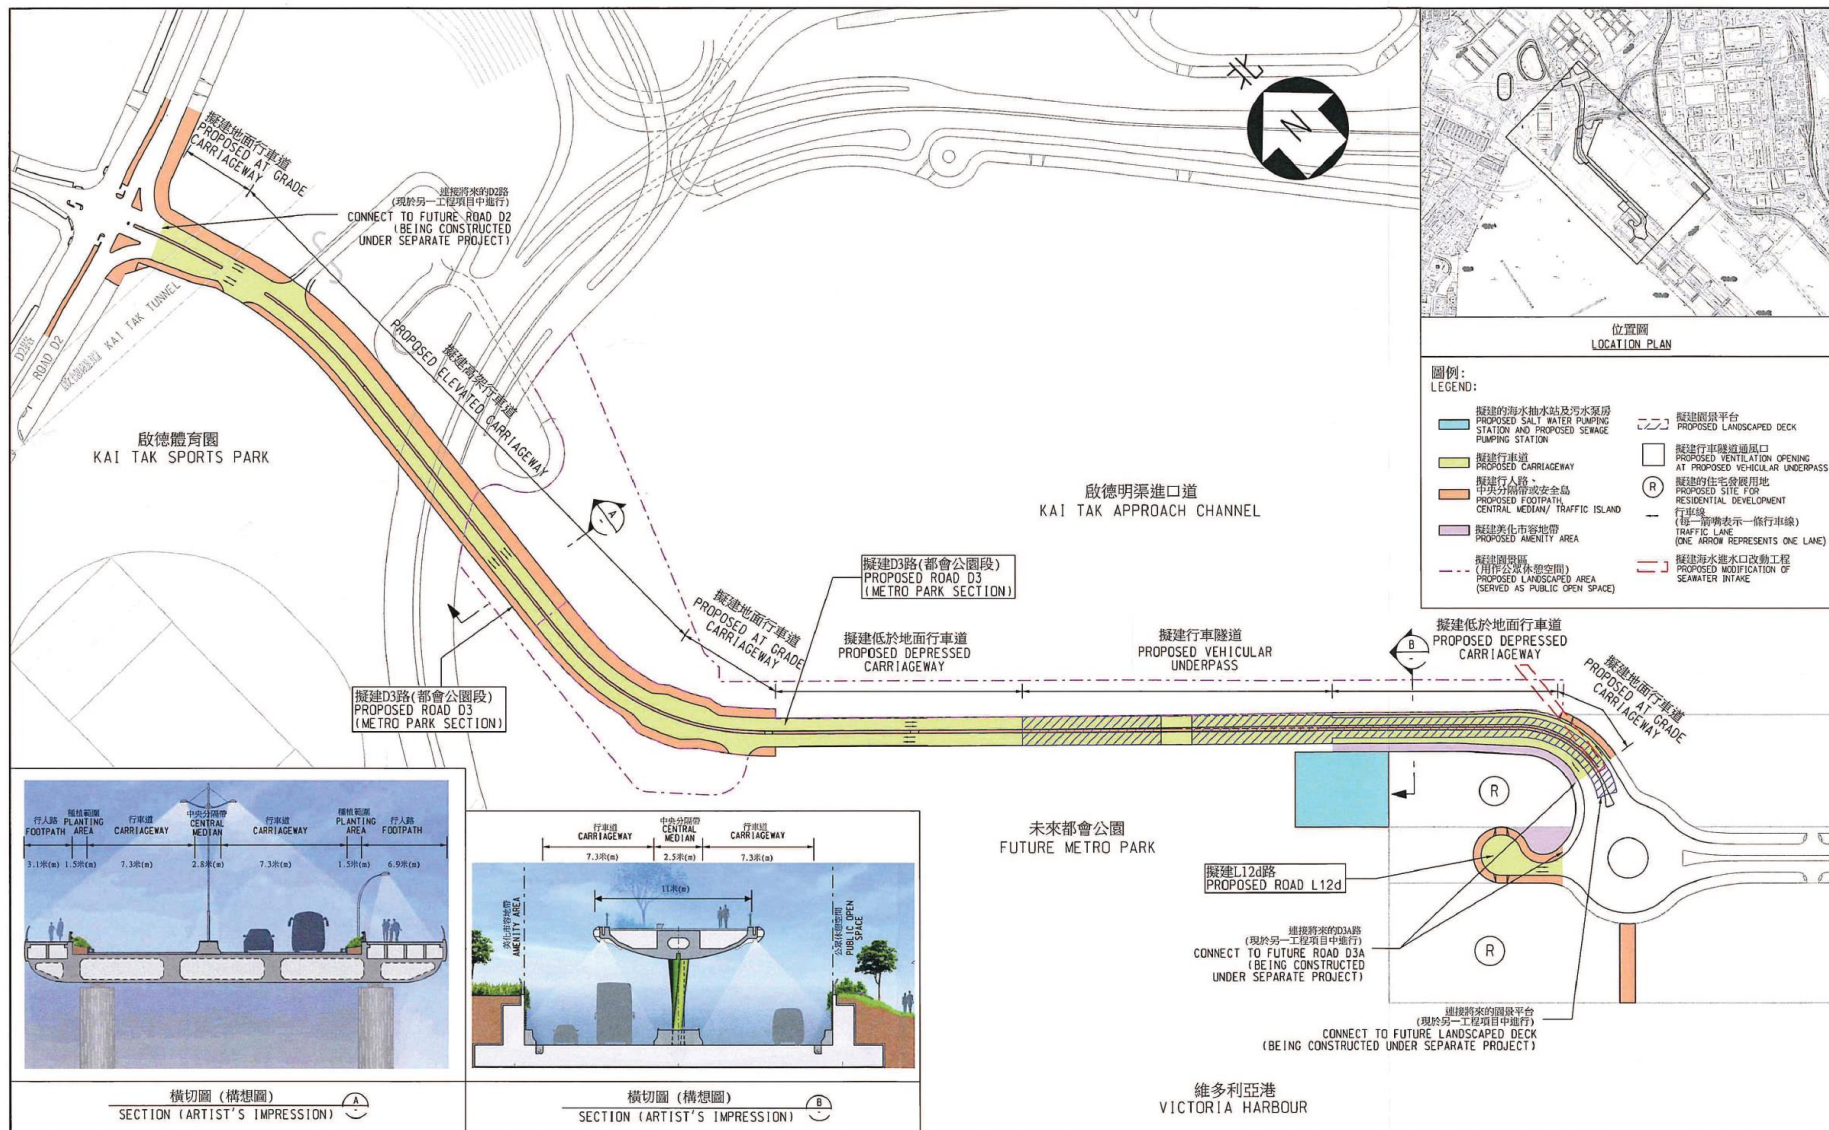


Figure 1 – Proposed works of Contract No. ED/2018/01

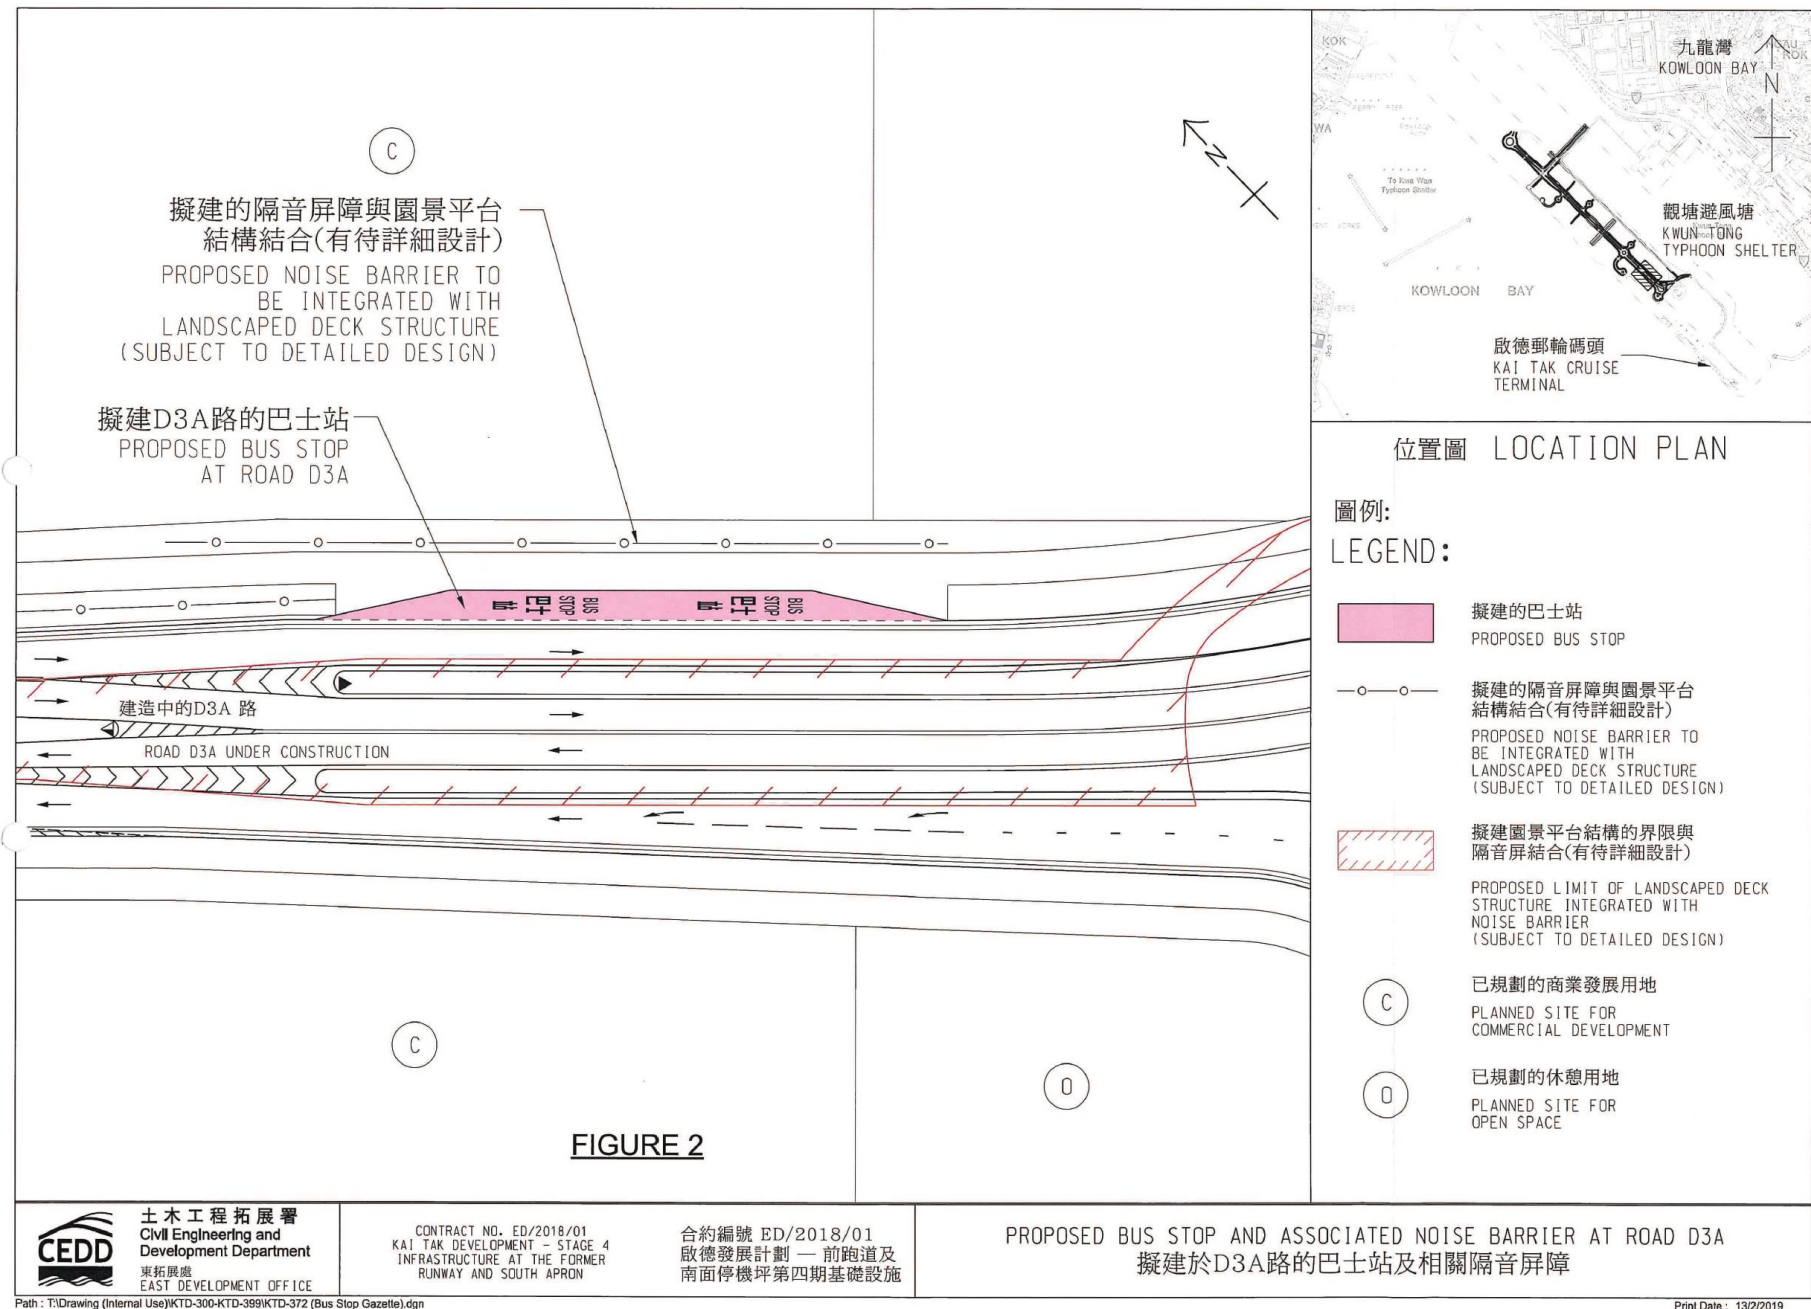


Figure 2 – Proposed Bus Stop And Associated Noise Barrier At Road D3A

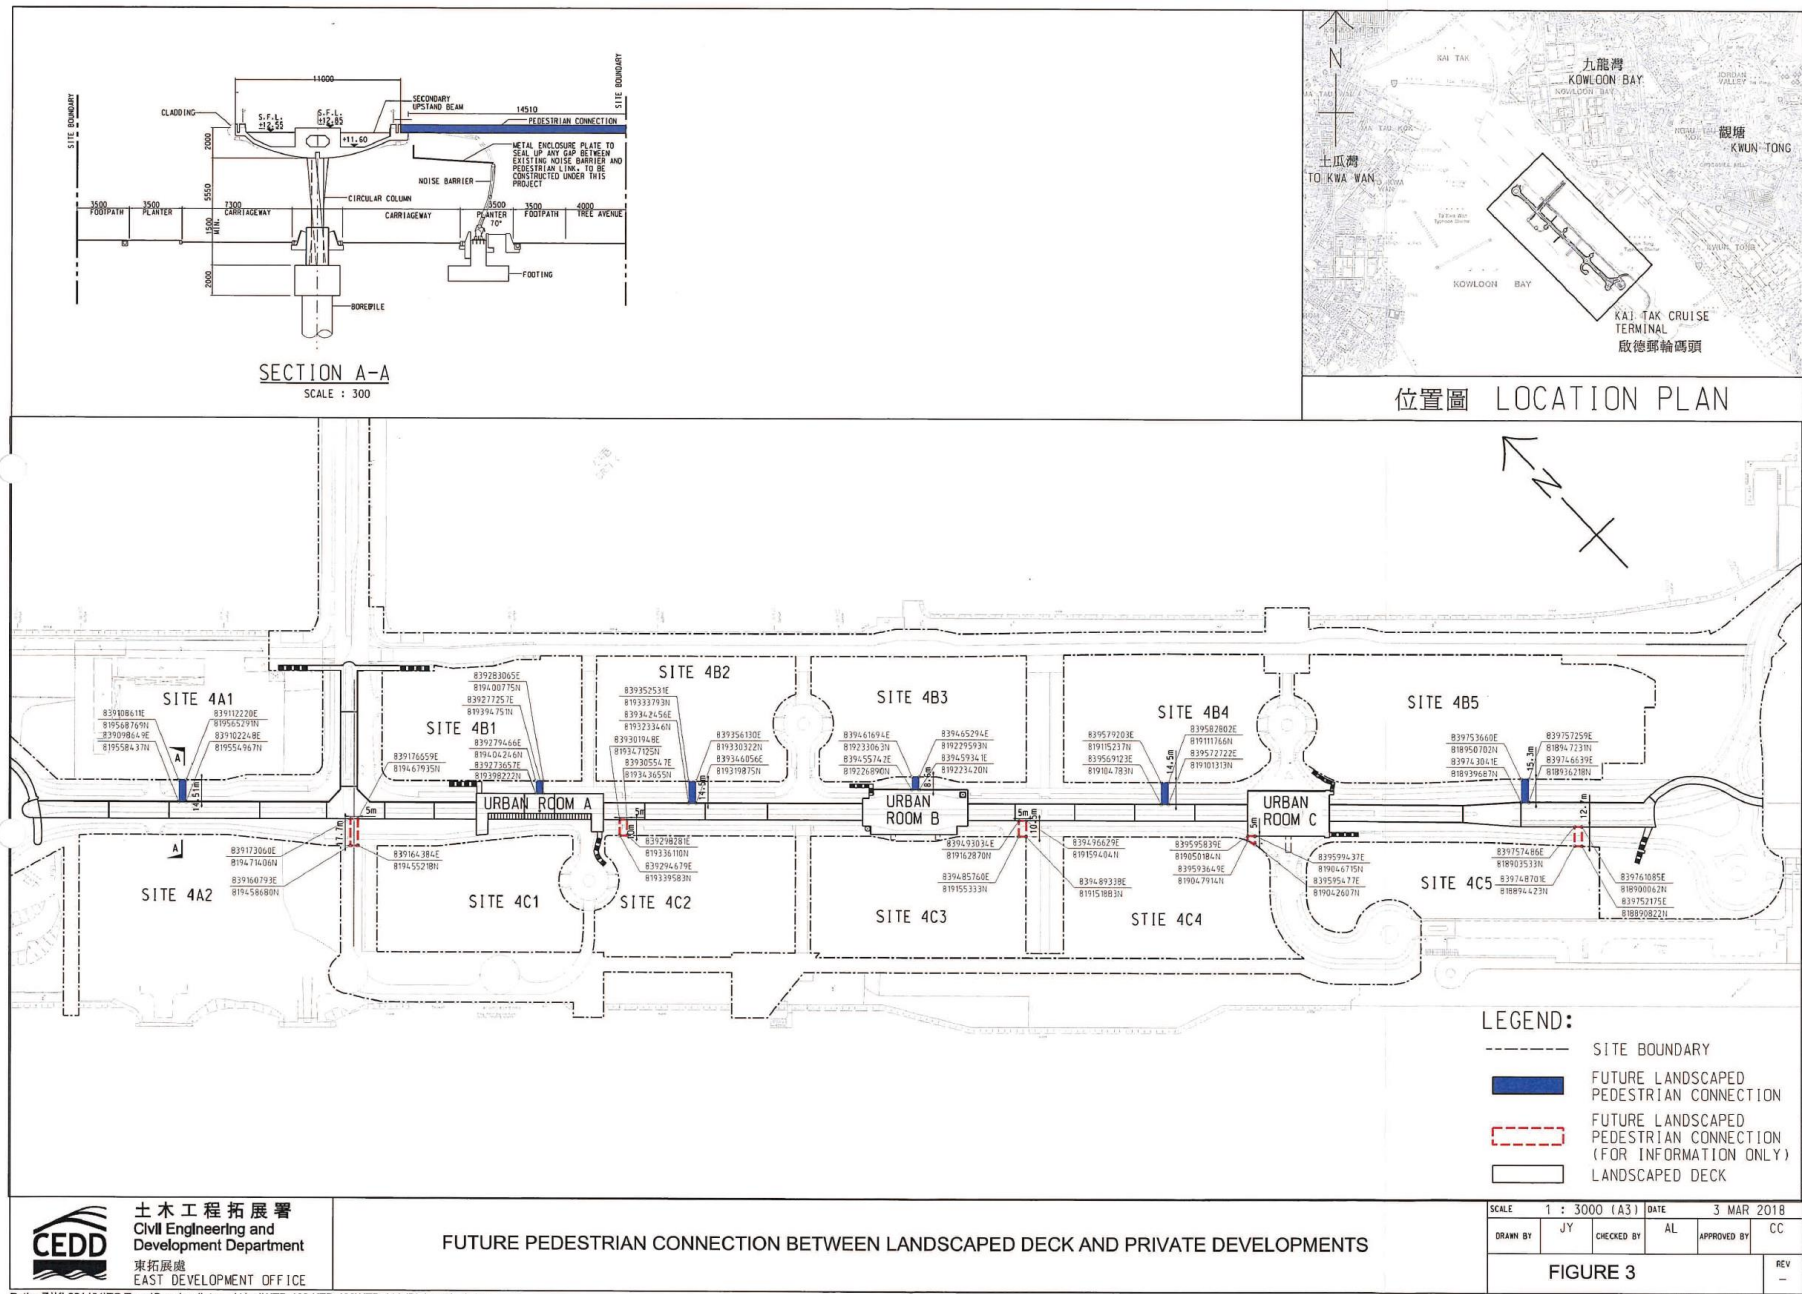


Figure 3 – Future Pedestrian Connection Between Landscaped Deck And Private Developments

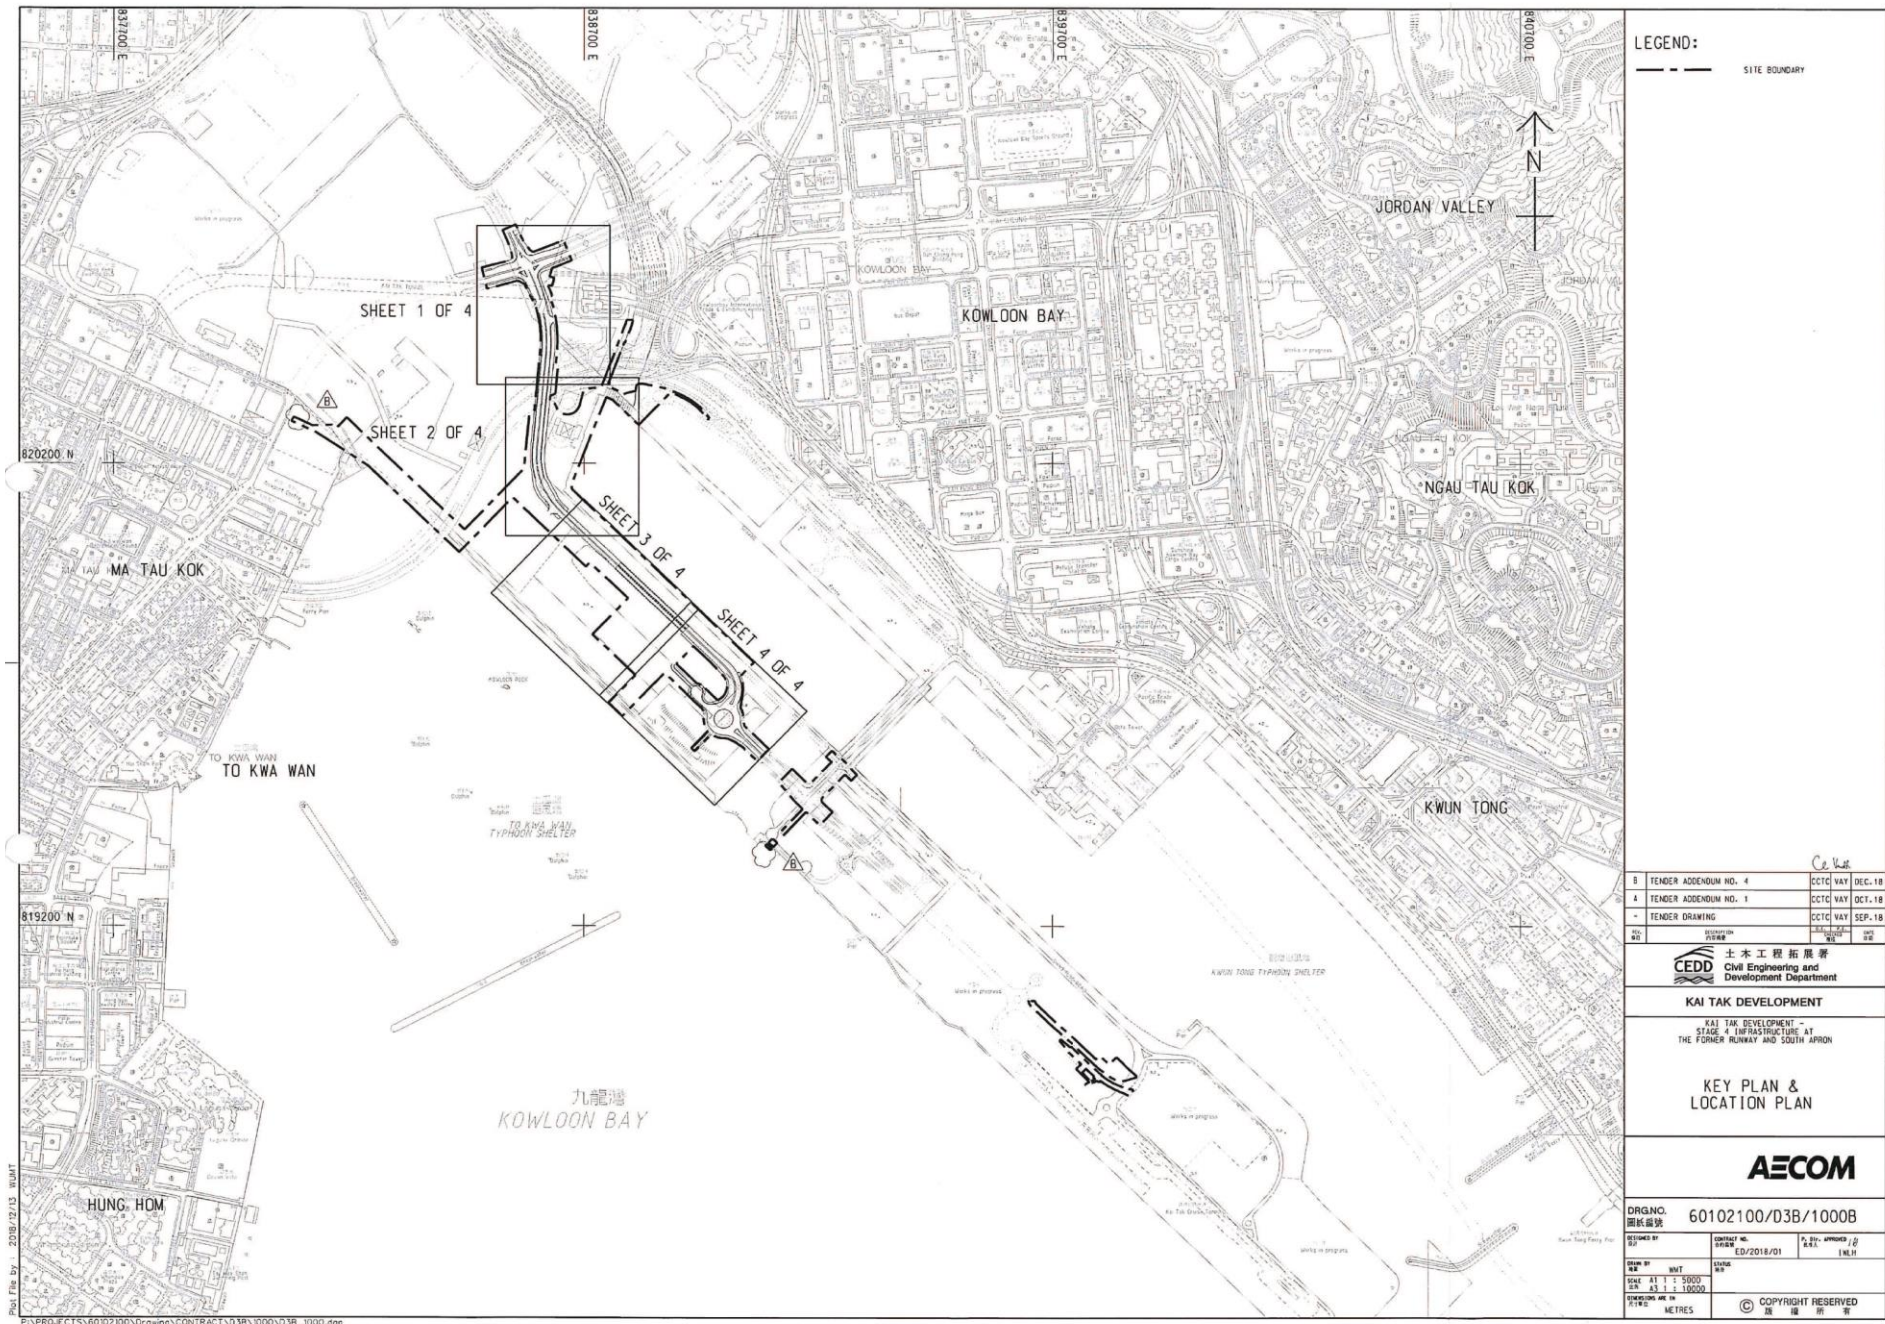


Figure 4 – Site Layout Plan

Special Traffic & Transport Arrangement

Notices on Clearways

Notices on Public Transports

Notices on Prohibited Zone

Notices on Temporary Speed Limits

Notices on Temporary Road Closure

Notices on Expressways

Other Notices

TRAFFIC NOTICES

TRANSPORT DEPARTMENT NOTICE

Temporary Traffic Arrangement on Newly Constructed Unnamed Road (Road D3 - (Metro Park Section)), Kowloon City

Notice is hereby given that the newly constructed unnamed road (Kai Tak Development - Road D3 (Metro Park Section)) connecting Shing Fung Road and Shing Kai Road/Muk Tai Street junction in Kowloon City District will be partially opened with effect from 2:00 p.m. on 31 December 2022.

Appropriate traffic signs will be erected on site to guide motorists.

LEE Sui-chun, Macella Commissioner for Transport (Acting)

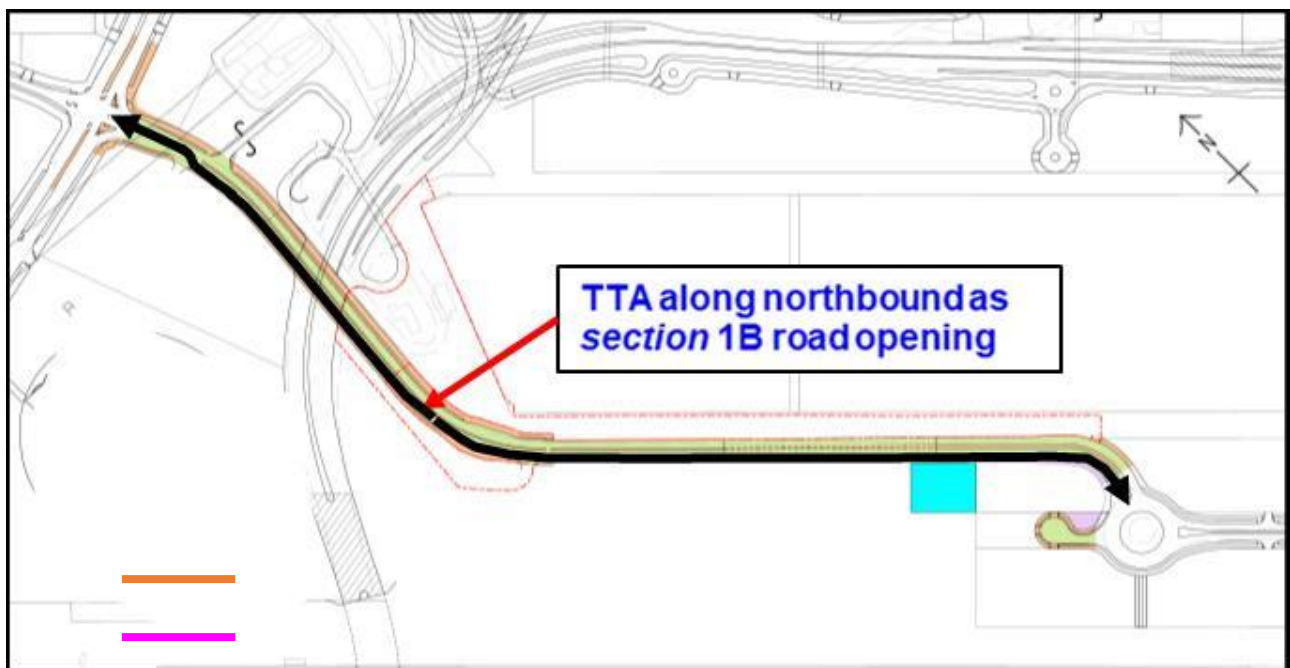


Figure 5 – New Opened Road on 31 December 2022

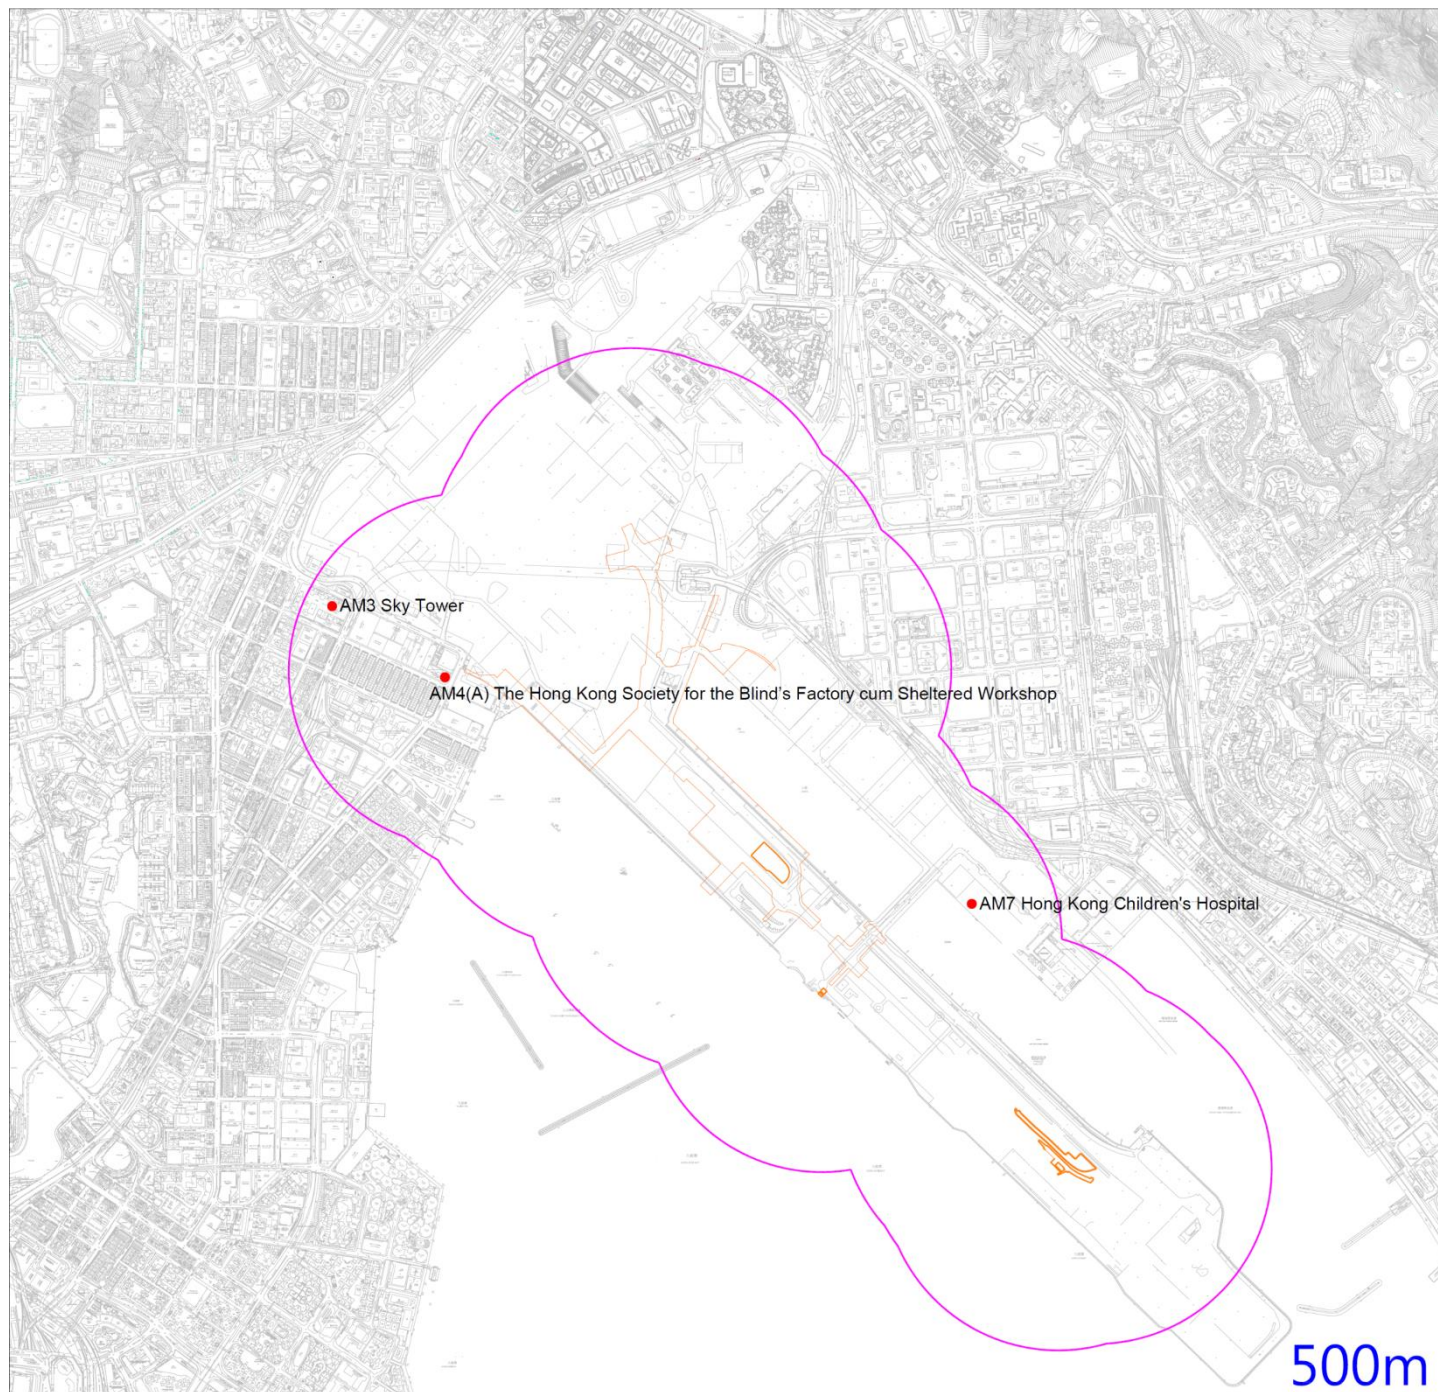


Figure 6 – Air Quality Monitoring Stations

* Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. Construction noise monitoring was conducted on the ground floor outside M11 with facing to the Project Site because of the access limitation in the reporting month.

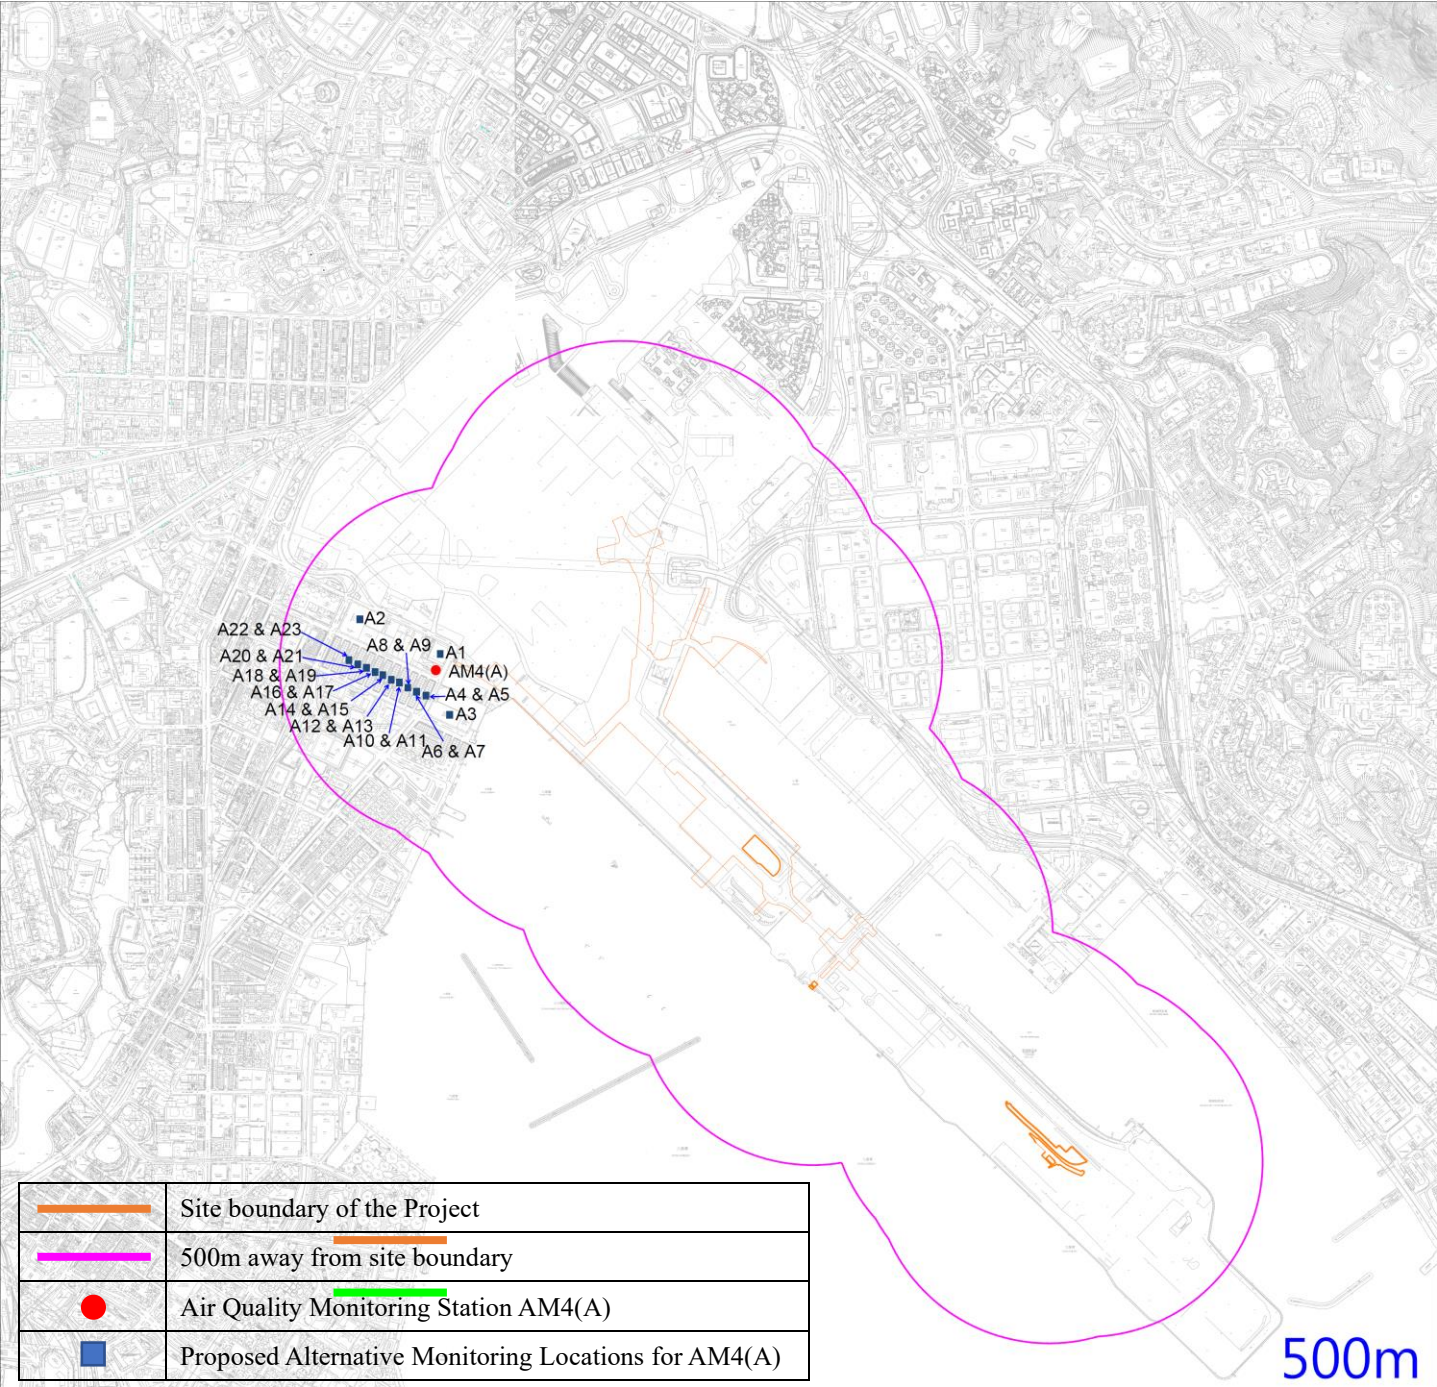


Figure 7 – Proposed Alternative Monitoring Locations for AM4(A)

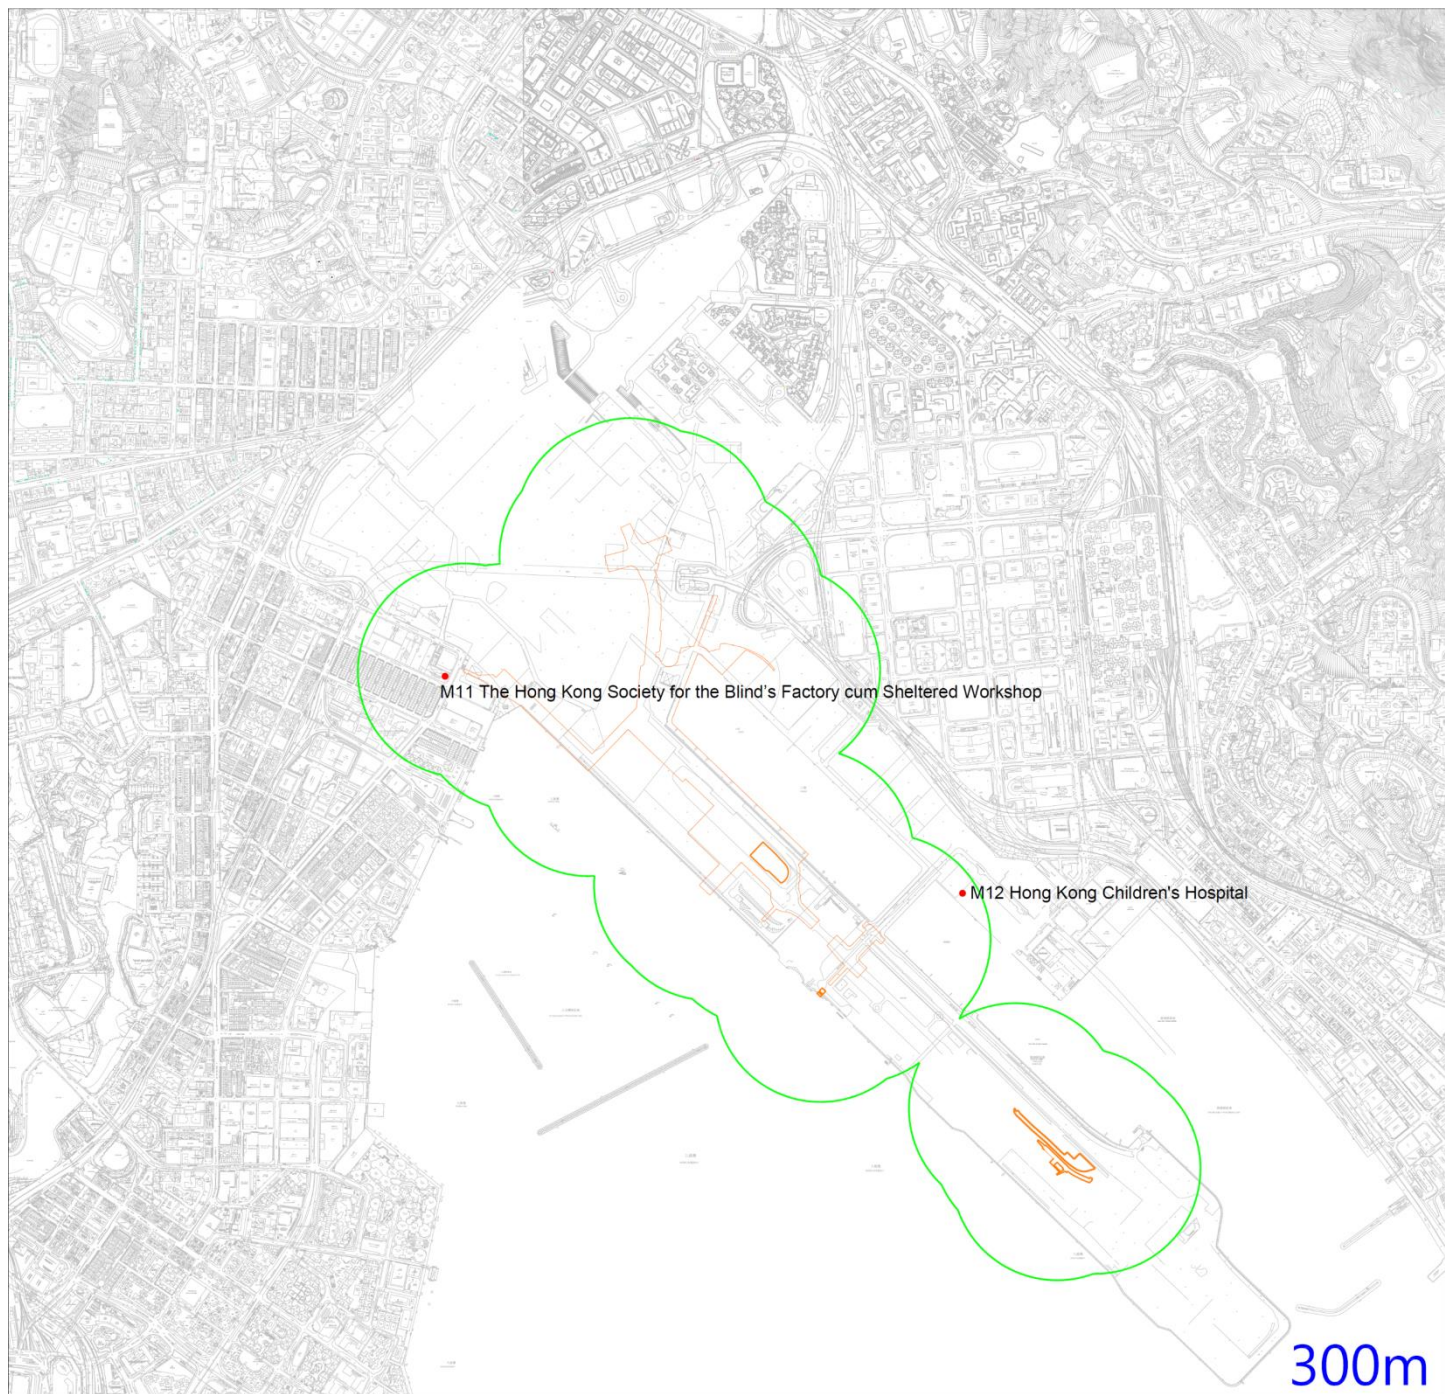


Figure 8 – Noise Monitoring Stations



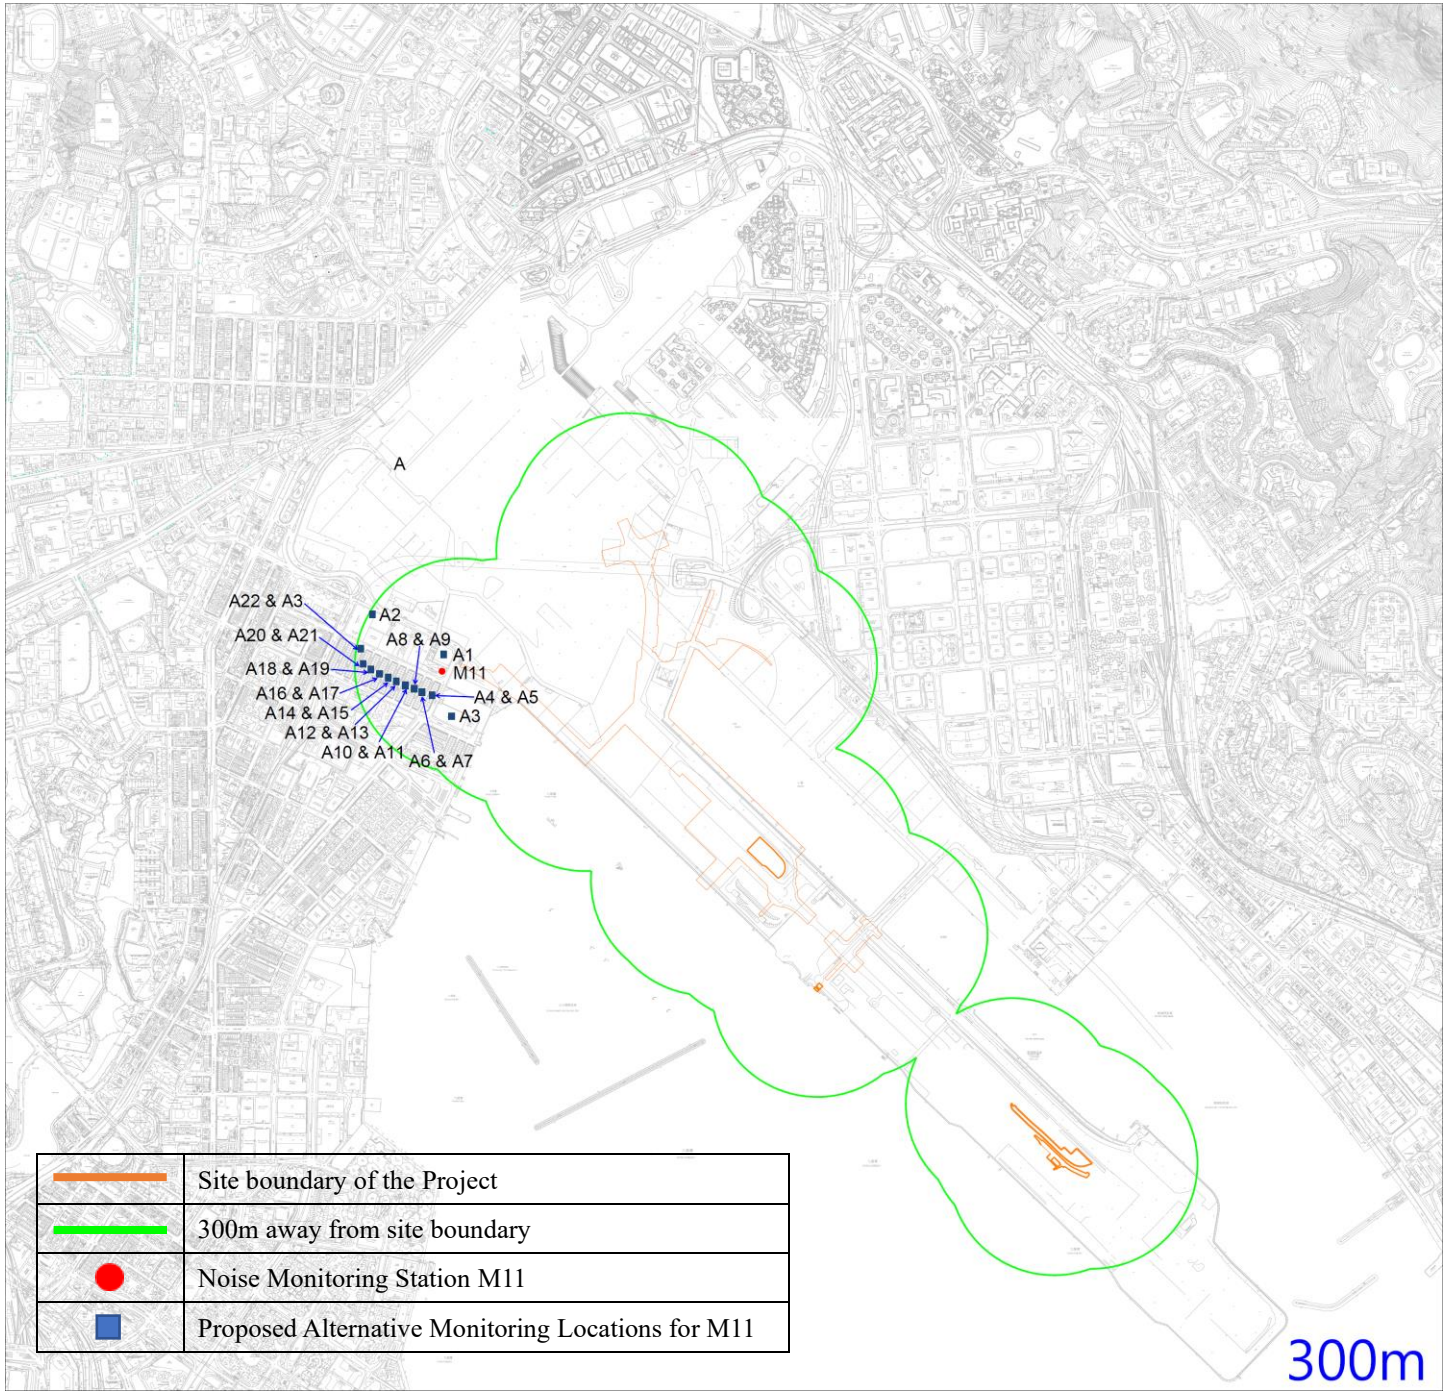



Figure 9 – Proposed Alternative Monitoring Locations for M11

Appendix A – Organization Chart of EM&A Team

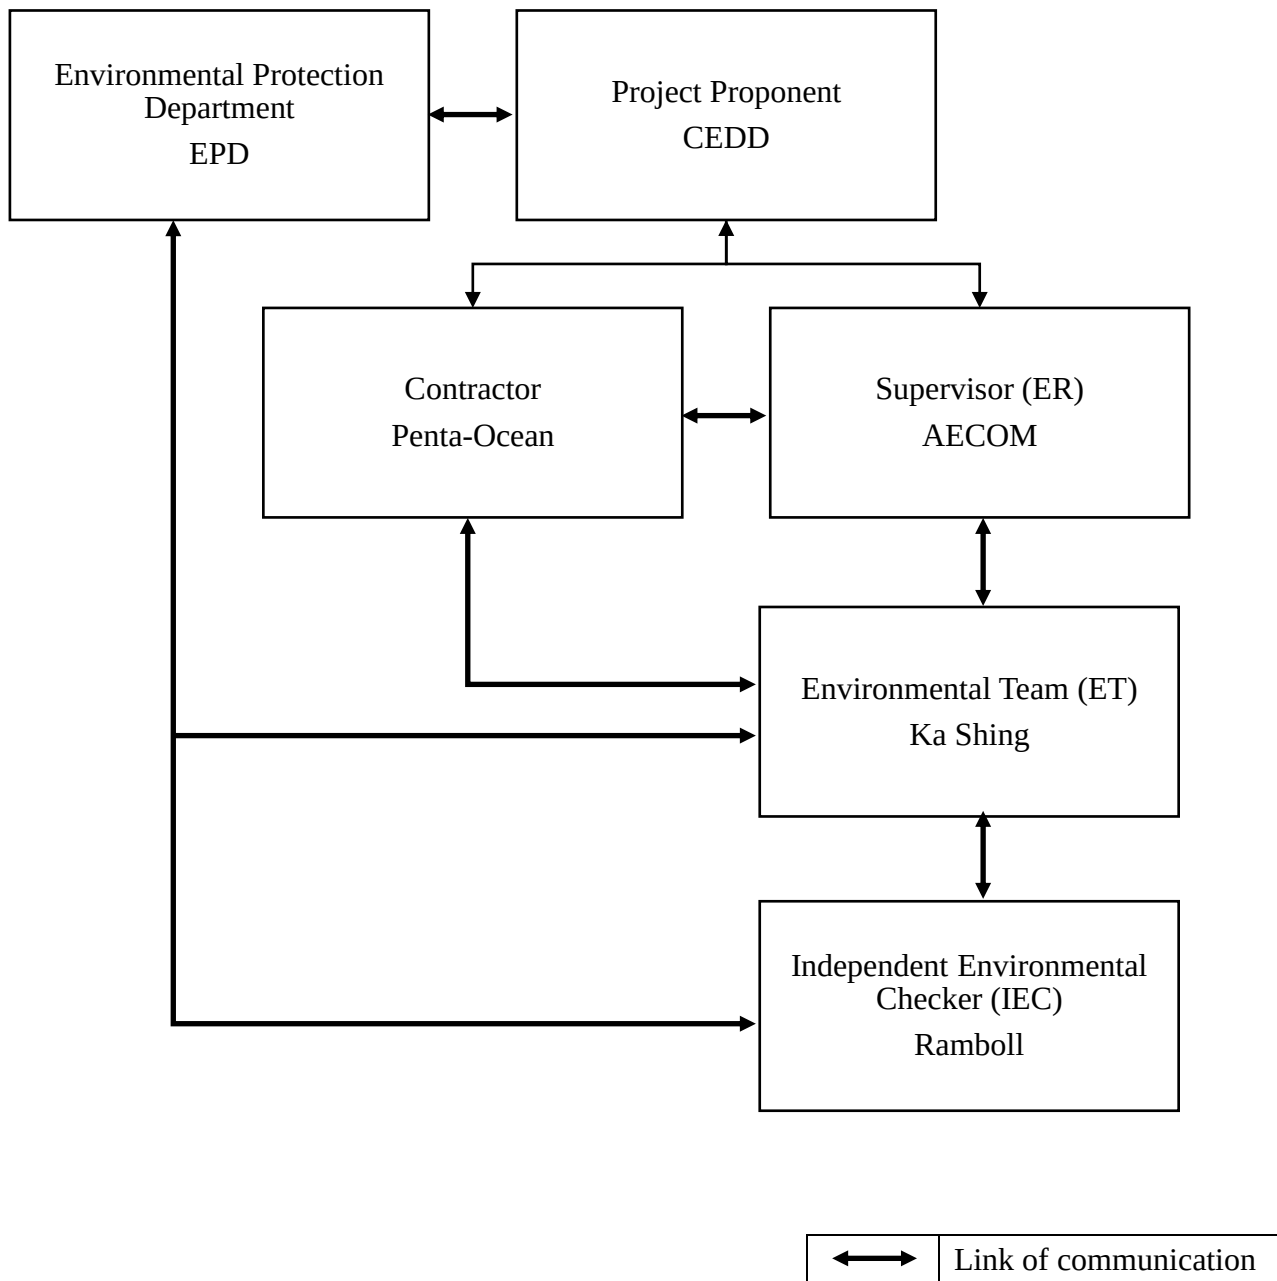

Appendix B – Construction Programme

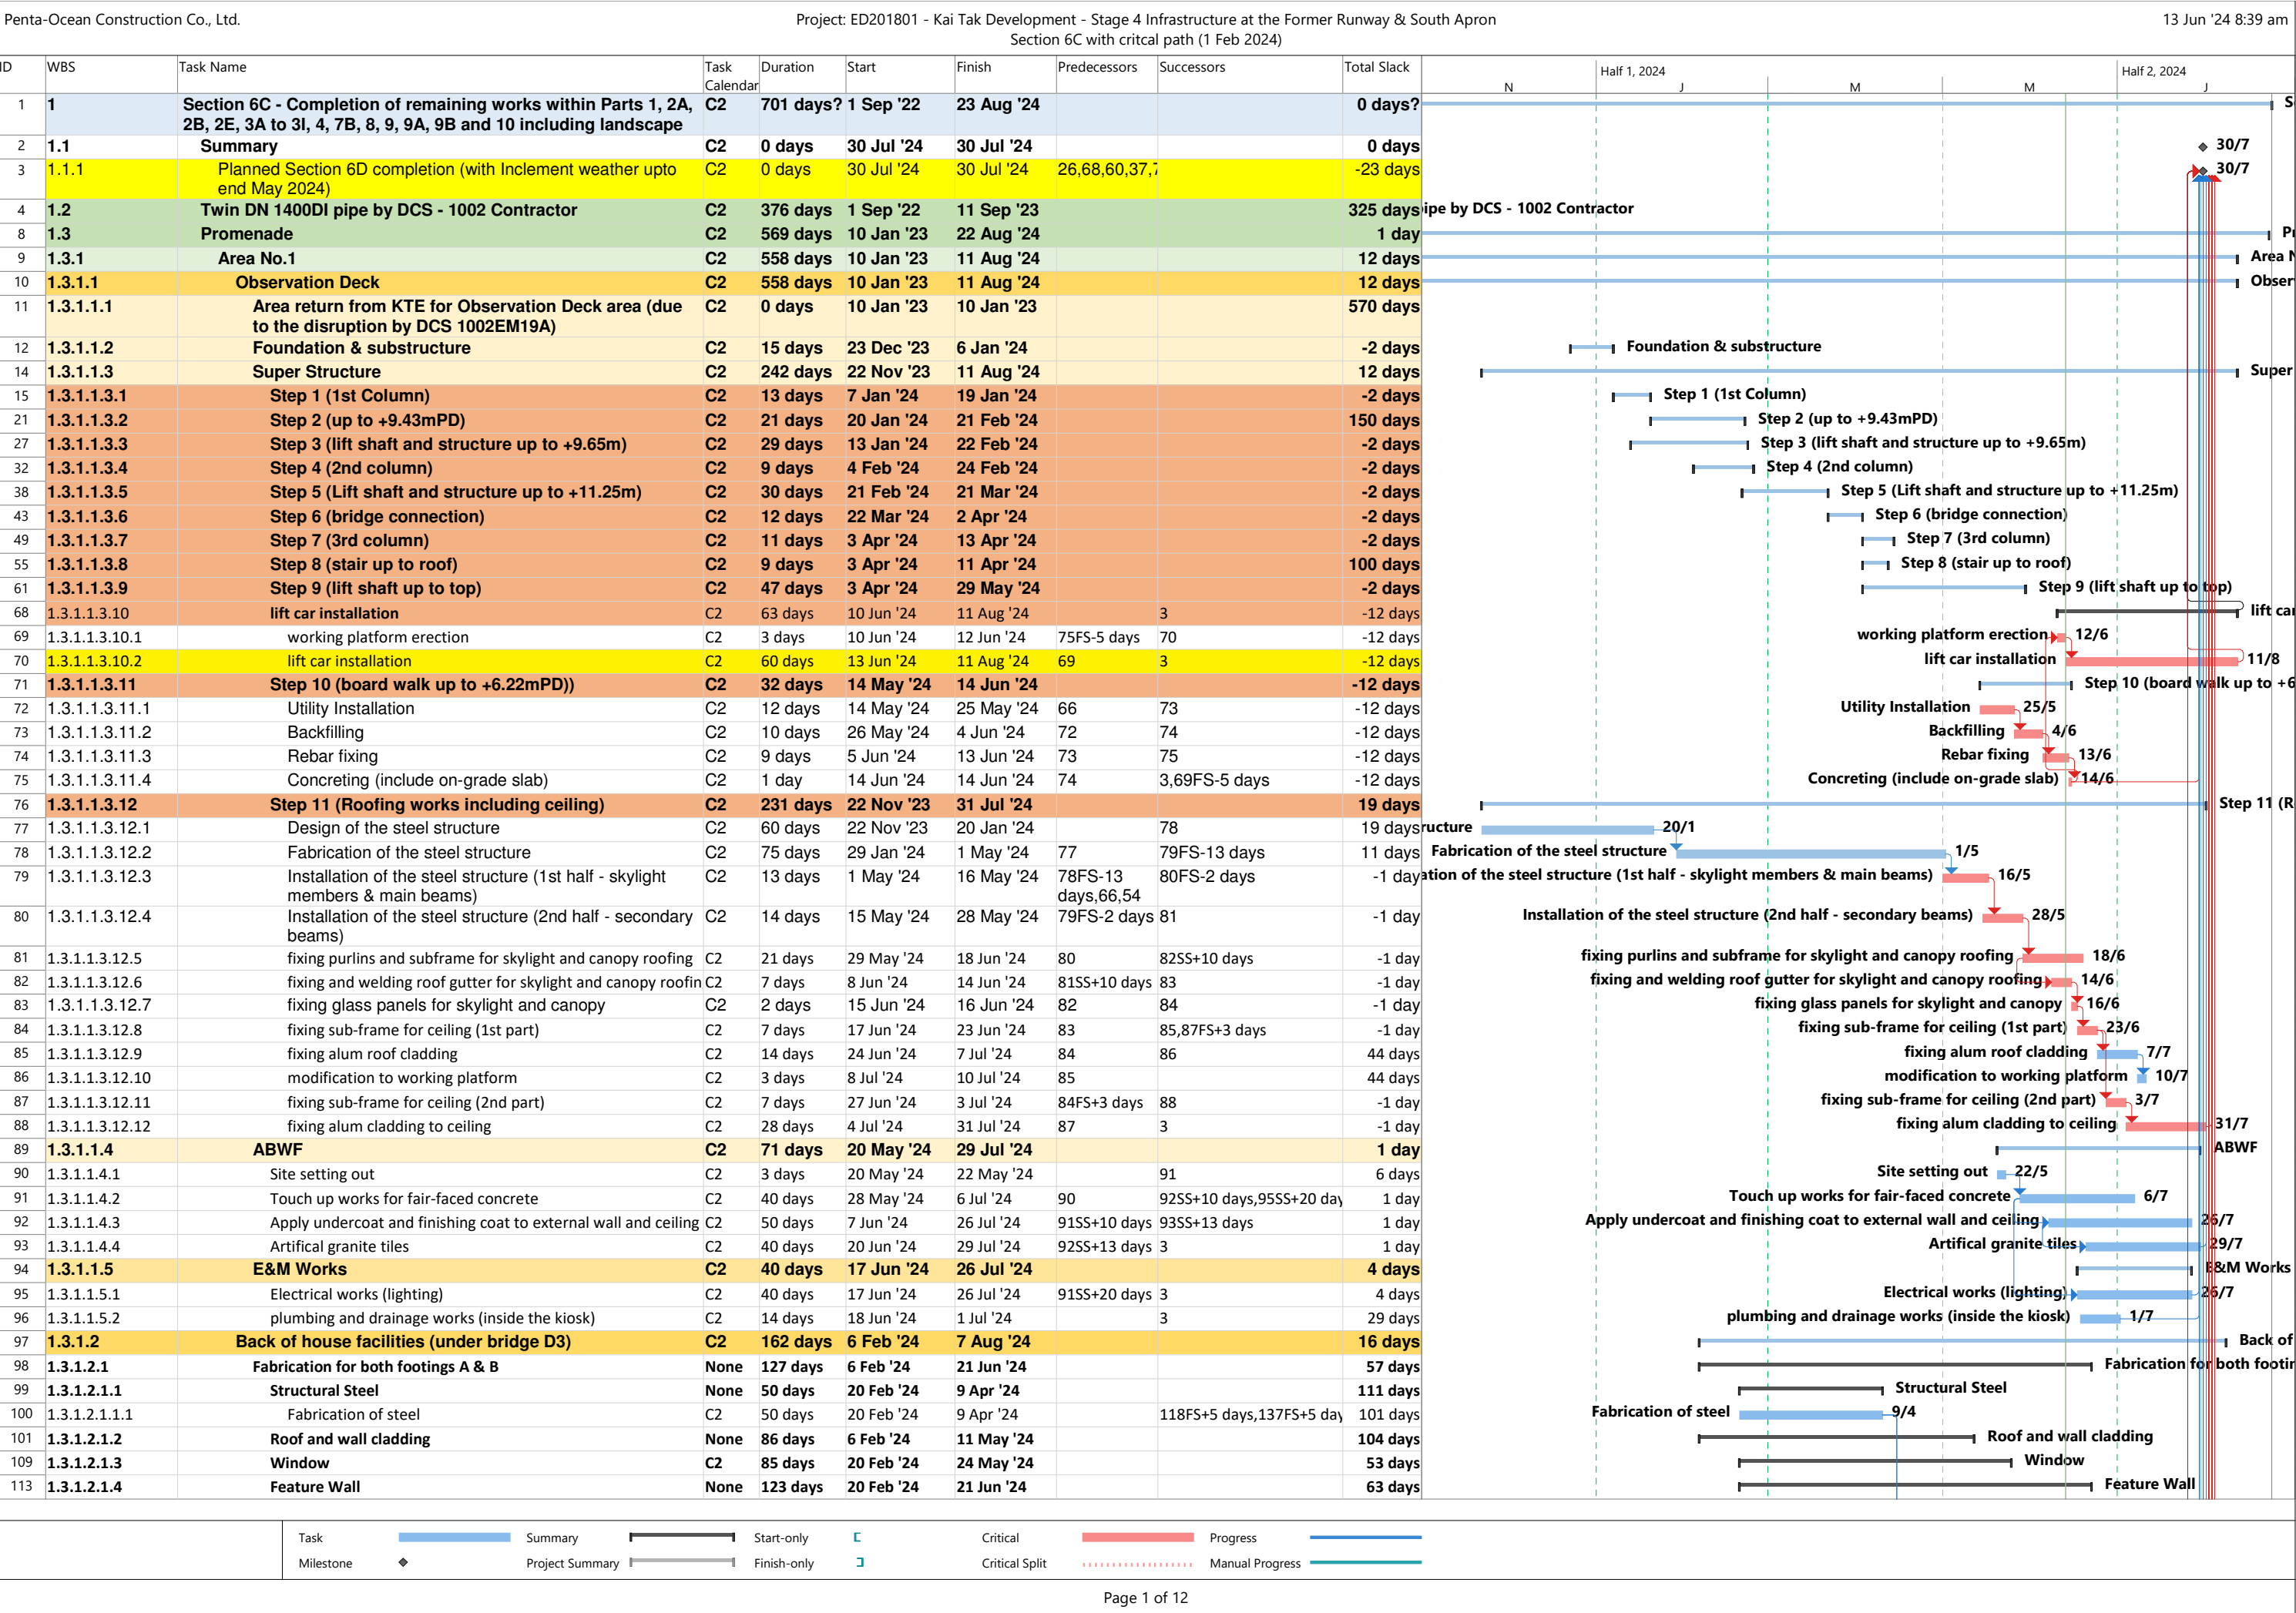

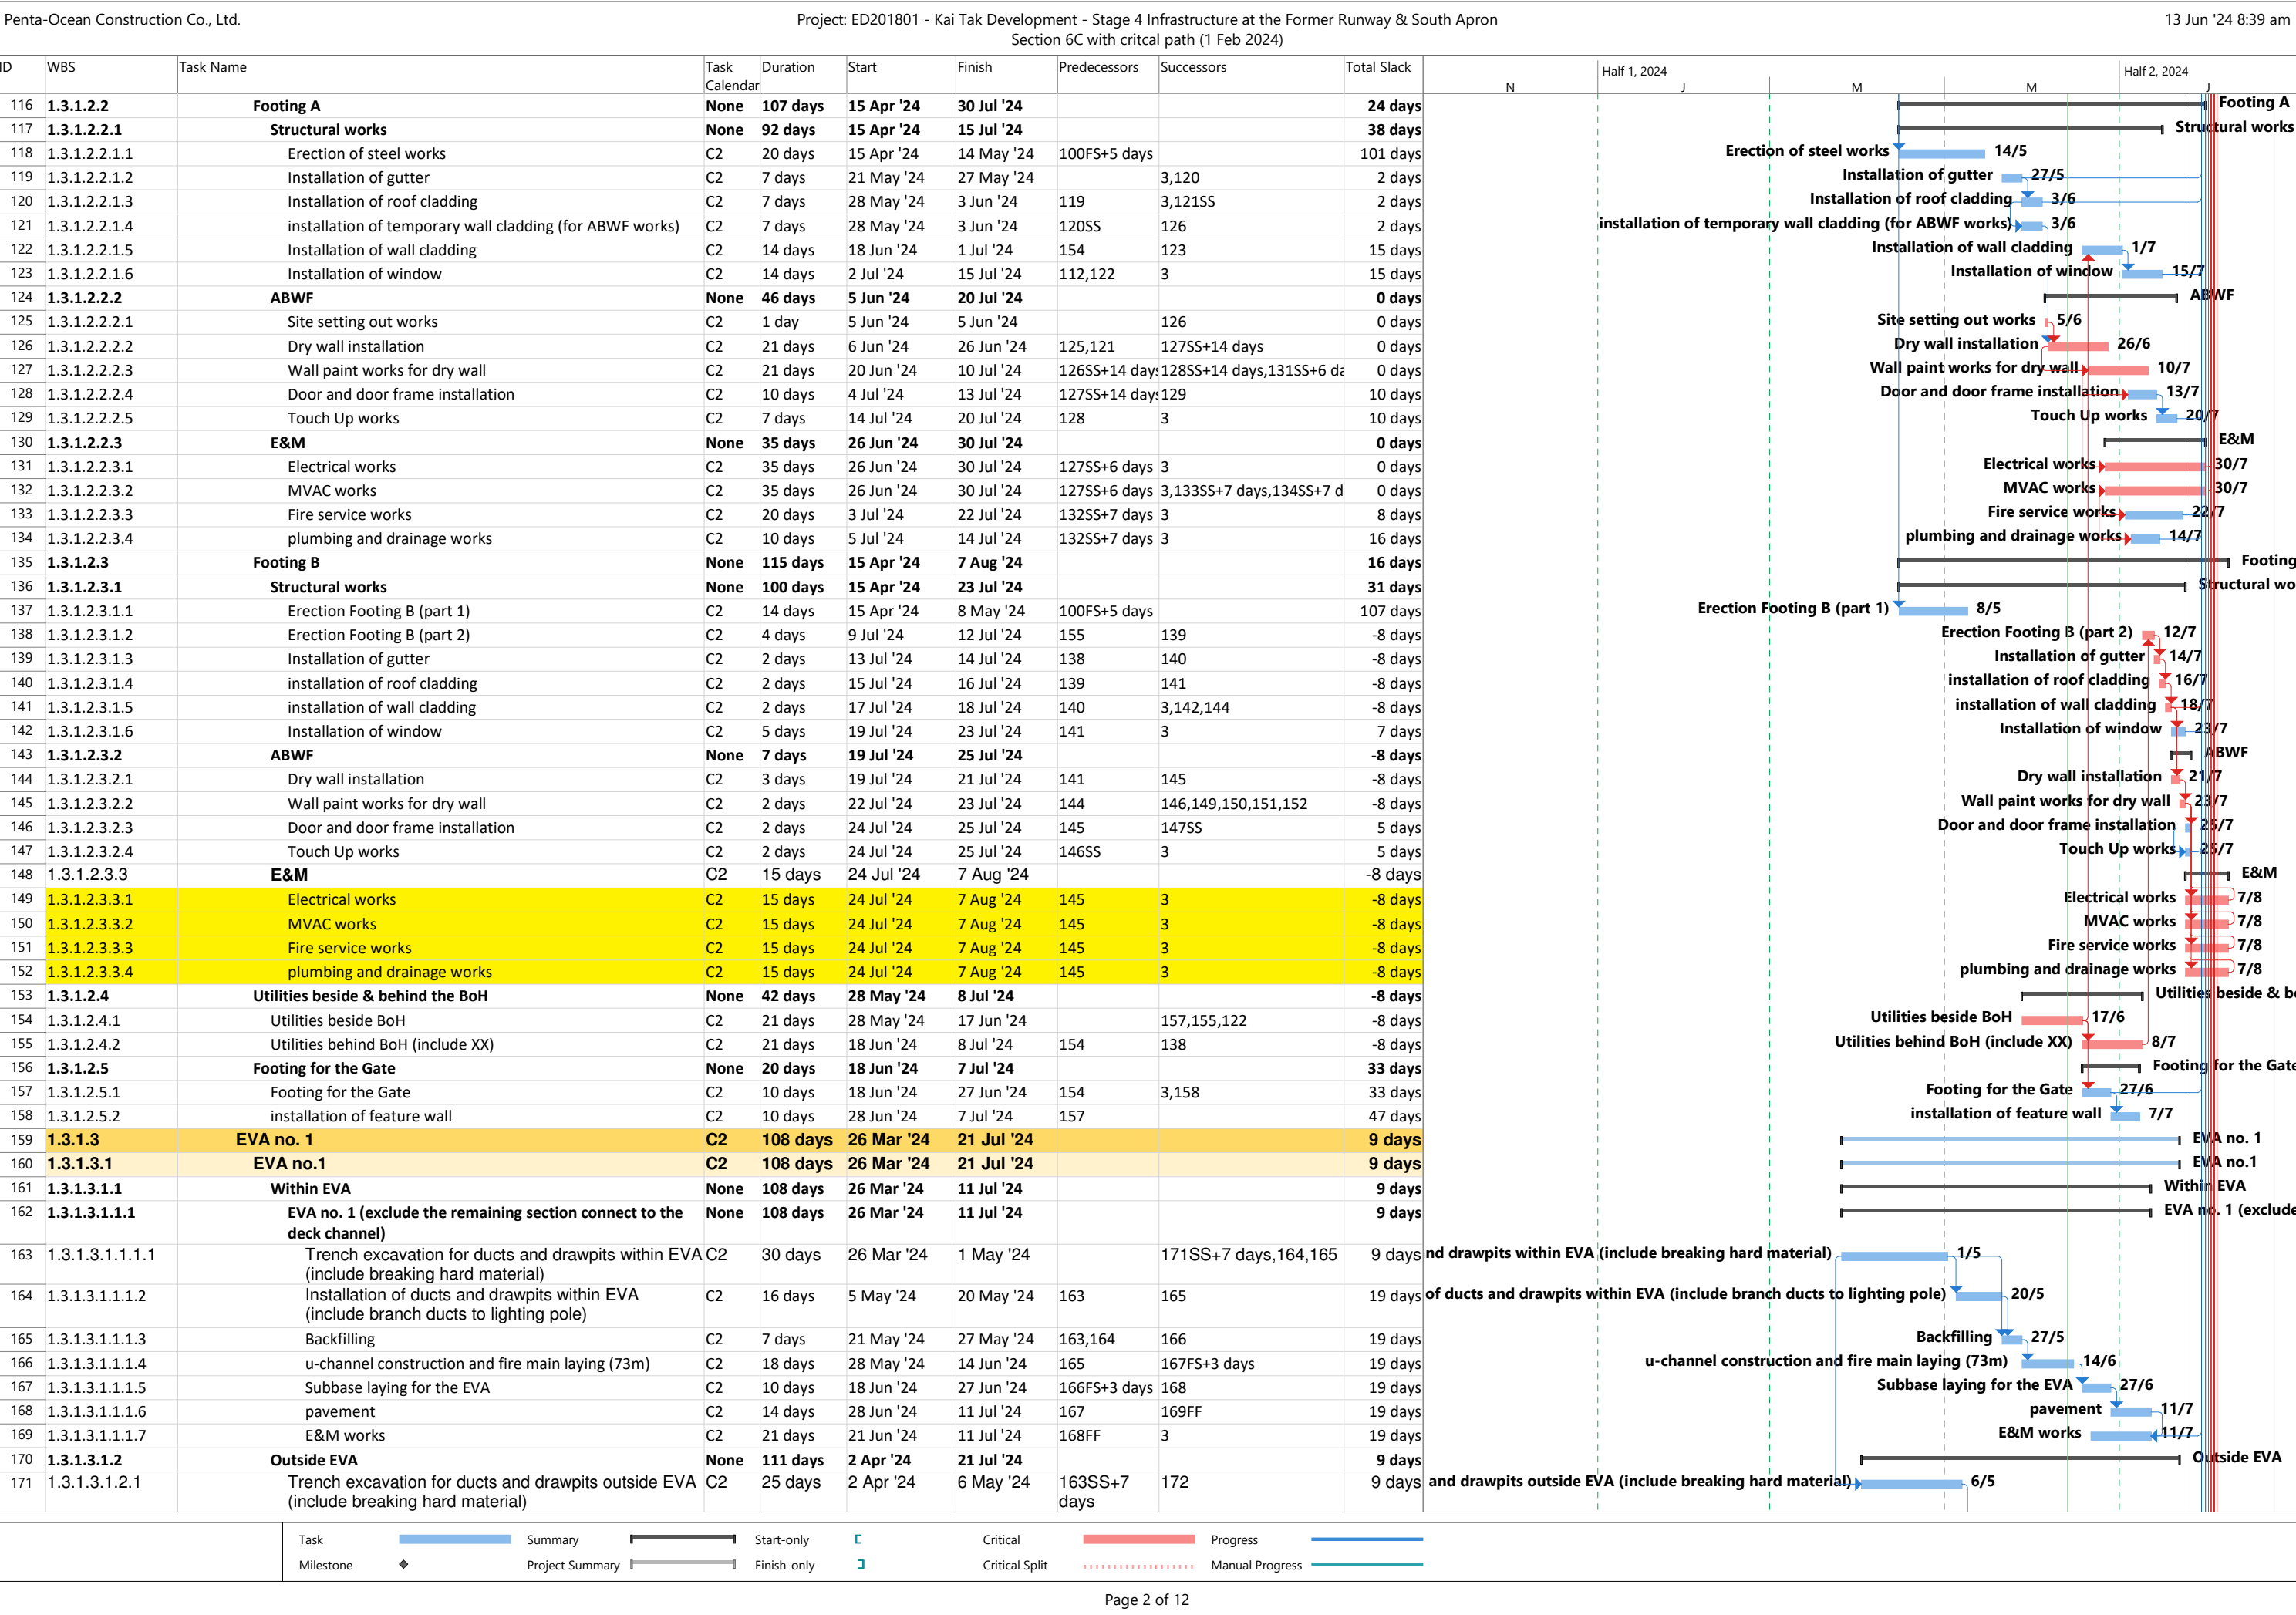

ID	WBS	Task Name	Task Calendar	Duration	Start	Finish	Predecessors	Successors	Total Slack		Half 1, 2024	Half 2, 2024
172	1.3.1.3.1.2.2	Installation of ducts and drawpits outside EVA	C2	18 days	7 May '24	24 May '24	171	173	9 days	N	Installation of ducts and drawpits outside EVA	24/5
173	1.3.1.3.1.2.3	Backfilling	C2	10 days	25 May '24	3 Jun '24	172	175FS+7 days	9 days		Backfilling	3/6
174	1.3.1.3.1.2.4	walkway construction	C2	41 days	11 Jun '24	21 Jul '24		3	9 days			walkway const
175	1.3.1.3.1.2.4.1	seawall cutting by Fong Cheong	C2	12 days	11 Jun '24	22 Jun '24	173FS+7 days	176	9 days		seawall cutting by Fong Cheong	22/6
176	1.3.1.3.1.2.4.2	glass balstrade installation (include E&M)	C2	14 days	23 Jun '24	6 Jul '24	175	177SS+8 days	9 days		glass balstrade installation (include E&M)	6/7
177	1.3.1.3.1.2.4.3	footpath	C2	21 days	1 Jul '24	21 Jul '24	176SS+8 days		9 days		footpath	21/7
178	1.3.1.4	Architectural /Hard landscaping Works	C2	45 days	1 Jun '24	15 Jul '24			12 days			Architectural /Ha
179	1.3.1.4.1	Fitness Lawn	C2	14 days	1 Jun '24	14 Jun '24			12 days		Fitness Lawn	
180	1.3.1.4.1.1	Excavation	C2	5 days	1 Jun '24	5 Jun '24		181FS+3 days	12 days		Excavation	5/6
181	1.3.1.4.1.2	Filling/ concreting	C2	6 days	9 Jun '24	14 Jun '24	180FS+3 day	3,183	12 days		Filling/ concreting	14/6
182	1.3.1.4.2	Event Deck	C2	14 days	15 Jun '24	28 Jun '24			12 days		Event Deck	
183	1.3.1.4.2.1	Excavation	C2	5 days	15 Jun '24	19 Jun '24	181	184FS+3 days,188SS	12 days		Excavation	19/6
184	1.3.1.4.2.2	Blinding concrete	C2	1 day	23 Jun '24	23 Jun '24	183FS+3 day	185	12 days		Blinding concrete	23/6
185	1.3.1.4.2.3	Rebar fixing	C2	4 days	24 Jun '24	27 Jun '24	184	186	12 days		Rebar fixing	27/6
186	1.3.1.4.2.4	Concreting	C2	1 day	28 Jun '24	28 Jun '24	185	3,193,340SS	12 days		Concreting	28/6
187	1.3.1.4.3	Dry Fountain	None	28 days	15 Jun '24	12 Jul '24			18 days		Dry Fountain	
188	1.3.1.4.3.1	Excavation	C2	3 days	15 Jun '24	17 Jun '24	183SS	189	18 days		Excavation	17/6
189	1.3.1.4.3.2	Filling/ concreting	C2	7 days	18 Jun '24	24 Jun '24	188	190	18 days		Filling/ concreting	24/6
190	1.3.1.4.3.3	Pipe, E&M	C2	12 days	25 Jun '24	6 Jul '24	189	191	18 days		Pipe, E&M	6/7
191	1.3.1.4.3.4	Cover	C2	6 days	7 Jul '24	12 Jul '24	190	3	18 days		Cover	12/7
192	1.3.1.4.4	Rain Garden	None	17 days	29 Jun '24	15 Jul '24			15 days		Rain Garden	
193	1.3.1.4.4.1	Excavation	C2	3 days	29 Jun '24	1 Jul '24	186	194	15 days		Excavation	1/7
194	1.3.1.4.4.2	Filling/plumbing/concreting	C2	14 days	2 Jul '24	15 Jul '24	193	3	15 days		Filling/plumbing/concreting	15/7
195	1.3.2	Area No. 2	C2	427 days	1 Jun '23	22 Aug '24			1 day			
196	1.3.2.1	Toilet cum changing room and Transformer Room	C2	427 days	1 Jun '23	22 Aug '24			1 day			
197	1.3.2.1.1	Structure (Toilet cum changing room and Transfomer FC	C2	247 days	1 Jun '23	2 Feb '24			181 days		Structure (Toilet cum changing room and Transfomer Room)	
198	1.3.2.1.1.1	ELS	C2	97 days	1 Jun '23	5 Sep '23			331 days			
201	1.3.2.1.1.2	Structural Works	C2	181 days	6 Aug '23	2 Feb '24			95 days		Structural Works	
221	1.3.2.1.2	Architectural Works	C2	185 days	29 Jan '24	22 Aug '24			-18 days			
222	1.3.2.1.2.1	Basement	None	104 days	30 Mar '24	11 Jul '24			24 days		Basement	
223	1.3.2.1.2.1.1	ABWF	None	99 days	30 Mar '24	6 Jul '24			24 days		ABWF	
224	1.3.2.1.2.1.1.1	wall & ceiling plastering	C2	28 days	30 Mar '24	6 May '24		225	71 days		wall & ceiling plastering	6/5
225	1.3.2.1.2.1.1.2	wall & ceiling painting	C2	14 days	7 May '24	20 May '24	224	3	71 days		wall & ceiling painting	20/5
226	1.3.2.1.2.1.1.3	floor screeding	C2	9 days	28 Jun '24	6 Jul '24	229FS-14 days	3	24 days		floor screeding	6/7
227	1.3.2.1.2.1.2	E&M	None	67 days	6 May '24	11 Jul '24			24 days		E&M	
228	1.3.2.1.2.1.2.1	MVAC works	C2	60 days	6 May '24	4 Jul '24		229SS+7 days	24 days		MVAC works	4/7
229	1.3.2.1.2.1.2.2	Electrical works	C2	60 days	13 May '24	11 Jul '24	228SS+7 days	226FS-14 days,230SS+7 da	24 days		Electrical works	11/7
230	1.3.2.1.2.1.2.3	Fire service works	C2	30 days	20 May '24	18 Jun '24	229SS+7 days	3	42 days		Fire service works	18/6
231	1.3.2.1.2.1.2.4	Plumbing and drainage works	C2	30 days	20 May '24	18 Jun '24	229SS+7 days	3	42 days		Plumbing and drainage works	18/6
232	1.3.2.1.2.2	G/F	C2	73 days	11 Jun '24	22 Aug '24			-23 days			
233	1.3.2.1.2.2.1	ABWF	C2	73 days	11 Jun '24	22 Aug '24			-23 days			
234	1.3.2.1.2.2.1.1	Block wall erection with steel frame	C2	10 days	18 Jun '24	27 Jun '24	235SS+7 day	236,241SS+10 days,246	-23 days		Block wall erection with steel frame	27/6
235	1.3.2.1.2.2.1.2	I-beam installation for baffle ceiling	C2	5 days	11 Jun '24	15 Jun '24		234SS+7 days	-23 days		I-beam installation for baffle ceiling	15/6
236	1.3.2.1.2.2.1.3	water-proofing work include 24h test at male toilet	C2	5 days	28 Jun '24	2 Jul '24	234	237	-5 days		water-proofing work include 24h test at male toilet	2/7
237	1.3.2.1.2.2.1.4	Wall plastering works at male toilet	C2	5 days	3 Jul '24	7 Jul '24	236	238FS-2 days,260,261	-5 days		Wall plastering works at male toilet	7/7
238	1.3.2.1.2.2.1.5	floor screeding works at male toilet	C2	5 days	6 Jul '24	10 Jul '24	237FS-2 day	239	-1 day		floor screeding works at male toilet	10/7
239	1.3.2.1.2.2.1.6	wall tiles laying at male toilet	C2	14 days	11 Jul '24	24 Jul '24	238	240FS-3 days	-1 day		wall tiles laying at male toilet	24/7
240	1.3.2.1.2.2.1.7	floor tiles at male toilet	C2	10 days	22 Jul '24	31 Jul '24	239FS-3 days	3	-1 day		floor tiles at male toilet	31/7
241	1.3.2.1.2.2.1.8	water-proofing work include 24h test at female toilet	C2	5 days	28 Jun '24	2 Jul '24	234SS+10 days	242	-23 days		water-proofing work include 24h test at female toilet	2/7
242	1.3.2.1.2.2.1.9	wall plastering works at female toilet	C2	6 days	3 Jul '24	8 Jul '24	241	243FS-2 days	-23 days		wall plastering works at female toilet	8/7
243	1.3.2.1.2.2.1.10	floor screeding works at female toilet	C2	5 days	7 Jul '24	11 Jul '24	242FS-2 day	248FS-2 days,244	-23 days		floor screeding works at female toilet	11/7
244	1.3.2.1.2.2.1.11	wall tiles laying at female toilet	C2	14 days	12 Jul '24	25 Jul '24	243	245FS-3 days	-2 days		wall tiles laying at female toilet	25/7
245	1.3.2.1.2.2.1.12	floor tiles laying at female toilet	C2	10 days	23 Jul '24	1 Aug '24	244FS-3 days	3	-2 days		floor tiles laying at female toilet	1/8
246	1.3.2.1.2.2.1.13	water-proofing work include 48 hr test at remaining area (baby care room; accessibility toilet etc	C2	7 days	14 Jul '24	20 Jul '24	234SS+26 days	247	7 days		water-proofing work include 48 hr test at remaining area (baby care room; accessibility toilet etc	20/7
247	1.3.2.1.2.2.1.14	wall plastering works at remaining area (baby care room; accessibility toilet etc	C2	3 days	21 Jul '24	23 Jul '24	246	3	7 days		wall plastering works at remaining area (baby care room; accessibility toilet etc	23/7
248	1.3.2.1.2.2.1.15	floor screeding works at remaining area (baby care room; accessibility toilet etc	C2	3 days	10 Jul '24	12 Jul '24	243FS-2 days	249,250FS-3 days,251	-23 days		floor screeding works at remaining area (baby care room; accessibility toilet etc	12/7

Task

Milestone

◆

Summary

Project Summary

Start-only

Finish-only

⌈

⌋


Critical

Critical Split

.....

Progress

Manual Progress

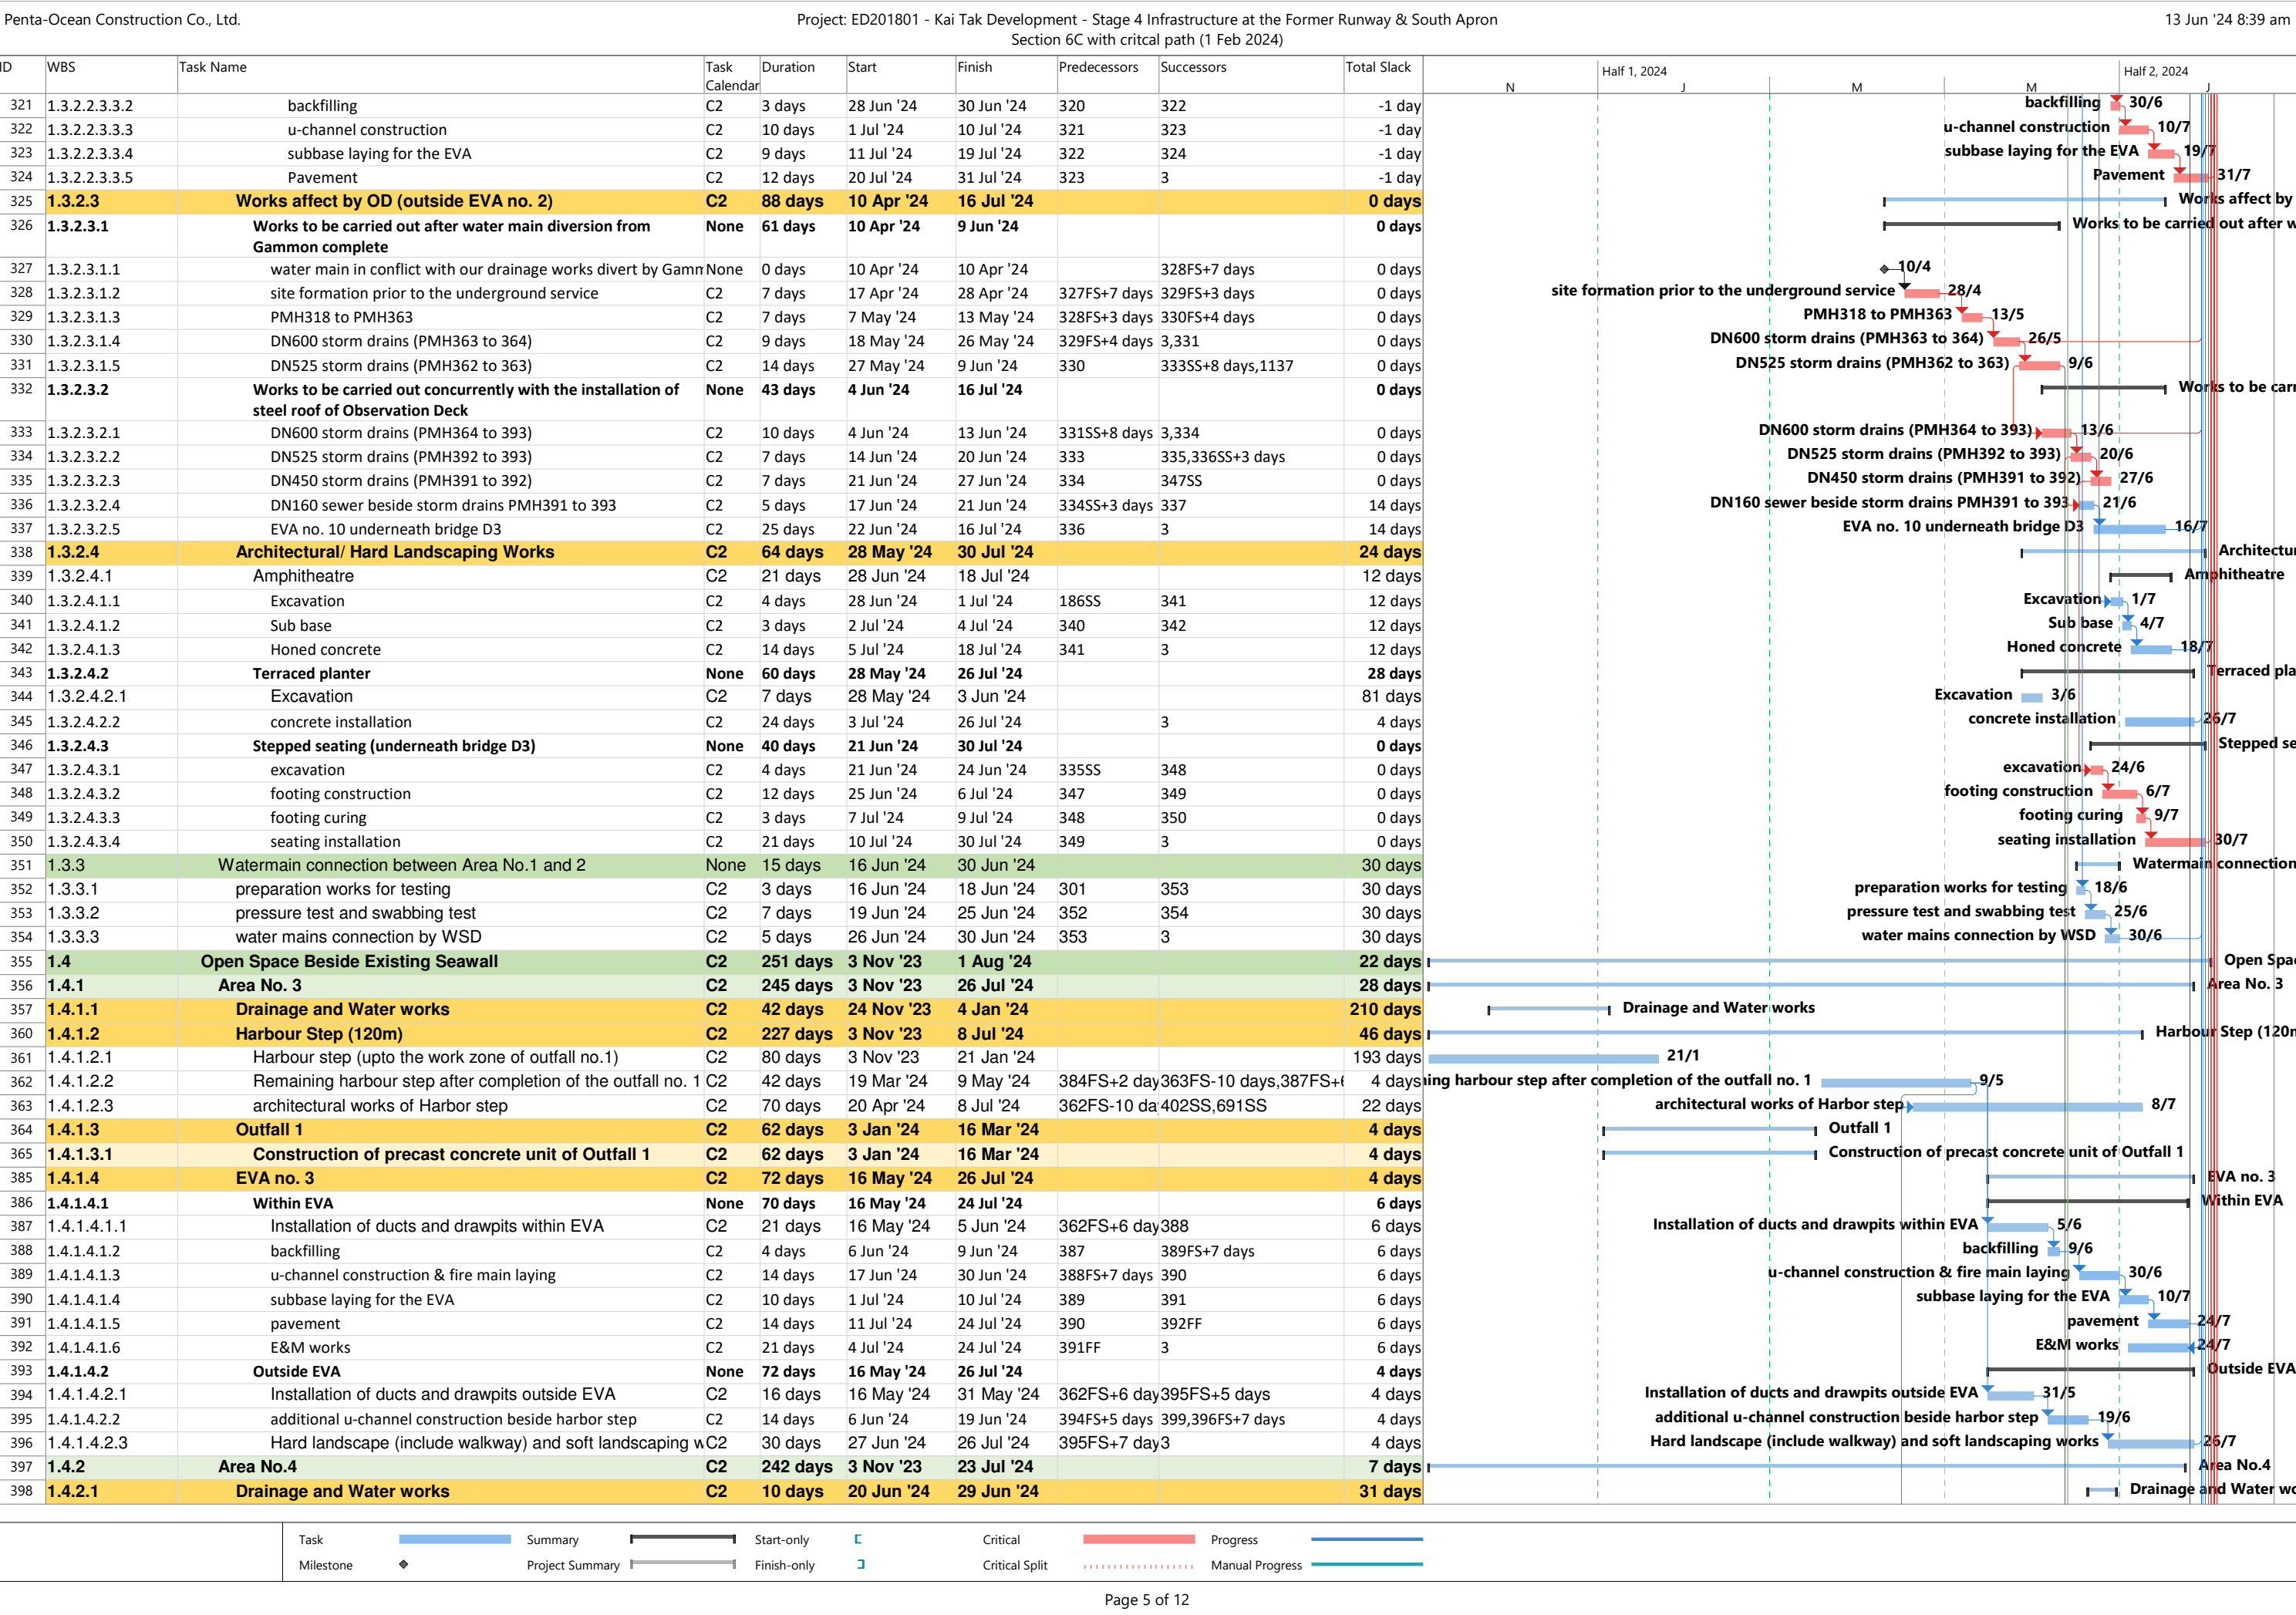

backfilling

u-channel construction

subbase laying for the EVA

Pavement

Works affect by OD (outside EVA no. 2)

Works to be carried out after water main diversion from Gammon complete

water main in conflict with our drainage works divert by Gammon

site formation prior to the underground service

PMH318 to PMH363

DN600 storm drains (PMH363 to 364)

DN525 storm drains (PMH362 to 363)

Works to be carried out concurrently with the installation of steel roof of Observation Deck

DN600 storm drains (PMH364 to 393)

DN525 storm drains (PMH392 to 393)

DN450 storm drains (PMH391 to 392)

DN160 sewer beside storm drains PMH391 to 393

EVA no. 10 underneath bridge D3

Architectural/ Hard Landscaping Works

Amphitheatre

Excavation

Sub base

Honed concrete

Terraced planter

Excavation

concrete installation

Stepped seating (underneath bridge D3)

excavation

footing construction

footing curing

seating installation

Watermain connection between Area No.1 and 2

preparation works for testing

pressure test and swabbing test

water mains connection by WSD

Open Space Beside Existing Seawall

Area No. 3

Drainage and Water works

Harbour Step (120m)

Harbour step (upto the work zone of outfall no.1)

Remaining harbour step after completion of the outfall no. 1

architectural works of Harbor step

Outfall 1

Construction of precast concrete unit of Outfall 1

EVA no. 3

Within EVA

Installation of ducts and drawpits within EVA

backfilling

u-channel construction & fire main laying

subbase laying for the EVA

pavement

E&M works

Outside EVA

Installation of ducts and drawpits outside EVA

additional u-channel construction beside harbor step

Hard landscape (include walkway) and soft landscaping works

Area No.4

Drainage and Water works

30/6

10/7

19/7

31/7

10/4

28/4

13/5

26/5

9/6

13/6

20/6

27/6

21/6

16/7

1/7

4/7

18/7

3/6

25/7

24/6

6/7

9/7

30/7

18/6

25/6

30/6

21/1

9/5

8/7

5/6

9/6

30/6

10/7

24/7

24/7

31/5

19/6

25/7

Works affect by

Works to be carried out after w

site formation prior to the underground service

PMH318 to PMH363

DN600 storm drains (PMH363 to 364)

DN525 storm drains (PMH362 to 363)

Works to be carr

DN600 storm drains (PMH364 to 393)

DN525 storm drains (PMH392 to 393)

DN450 storm drains (PMH391 to 392)

DN160 sewer beside storm drains PMH391 to 393

EVA no. 10 underneath bridge D3

Architectur

Amphitheatre

Excavation

Sub base

Honed concrete

Terraced pla

Excavation

concrete installation

Stepped se

excavation

footing construction

footing curing

seating installation

Watermain connection

preparation works for testing

pressure test and swabbing test

water mains connection by WSD

Open Spac

Area No. 3

Drainage and Water works

Harbour Step (120n

ing harbour step after completion of the outfall no. 1

architectural works of Harbor step

Outfall 1

Construction of precast concrete unit of Outfall 1

EVA no. 3

Within EVA

Installation of ducts and drawpits within EVA

backfilling

u-channel construction & fire main laying

subbase laying for the EVA

pavement

E&M works

Outside EVA

Installation of ducts and drawpits outside EVA


additional u-channel construction beside harbor step

Hard landscape (include walkway) and soft landscaping works

Area No.4


Drainage and Water wc

Page 5 of 12

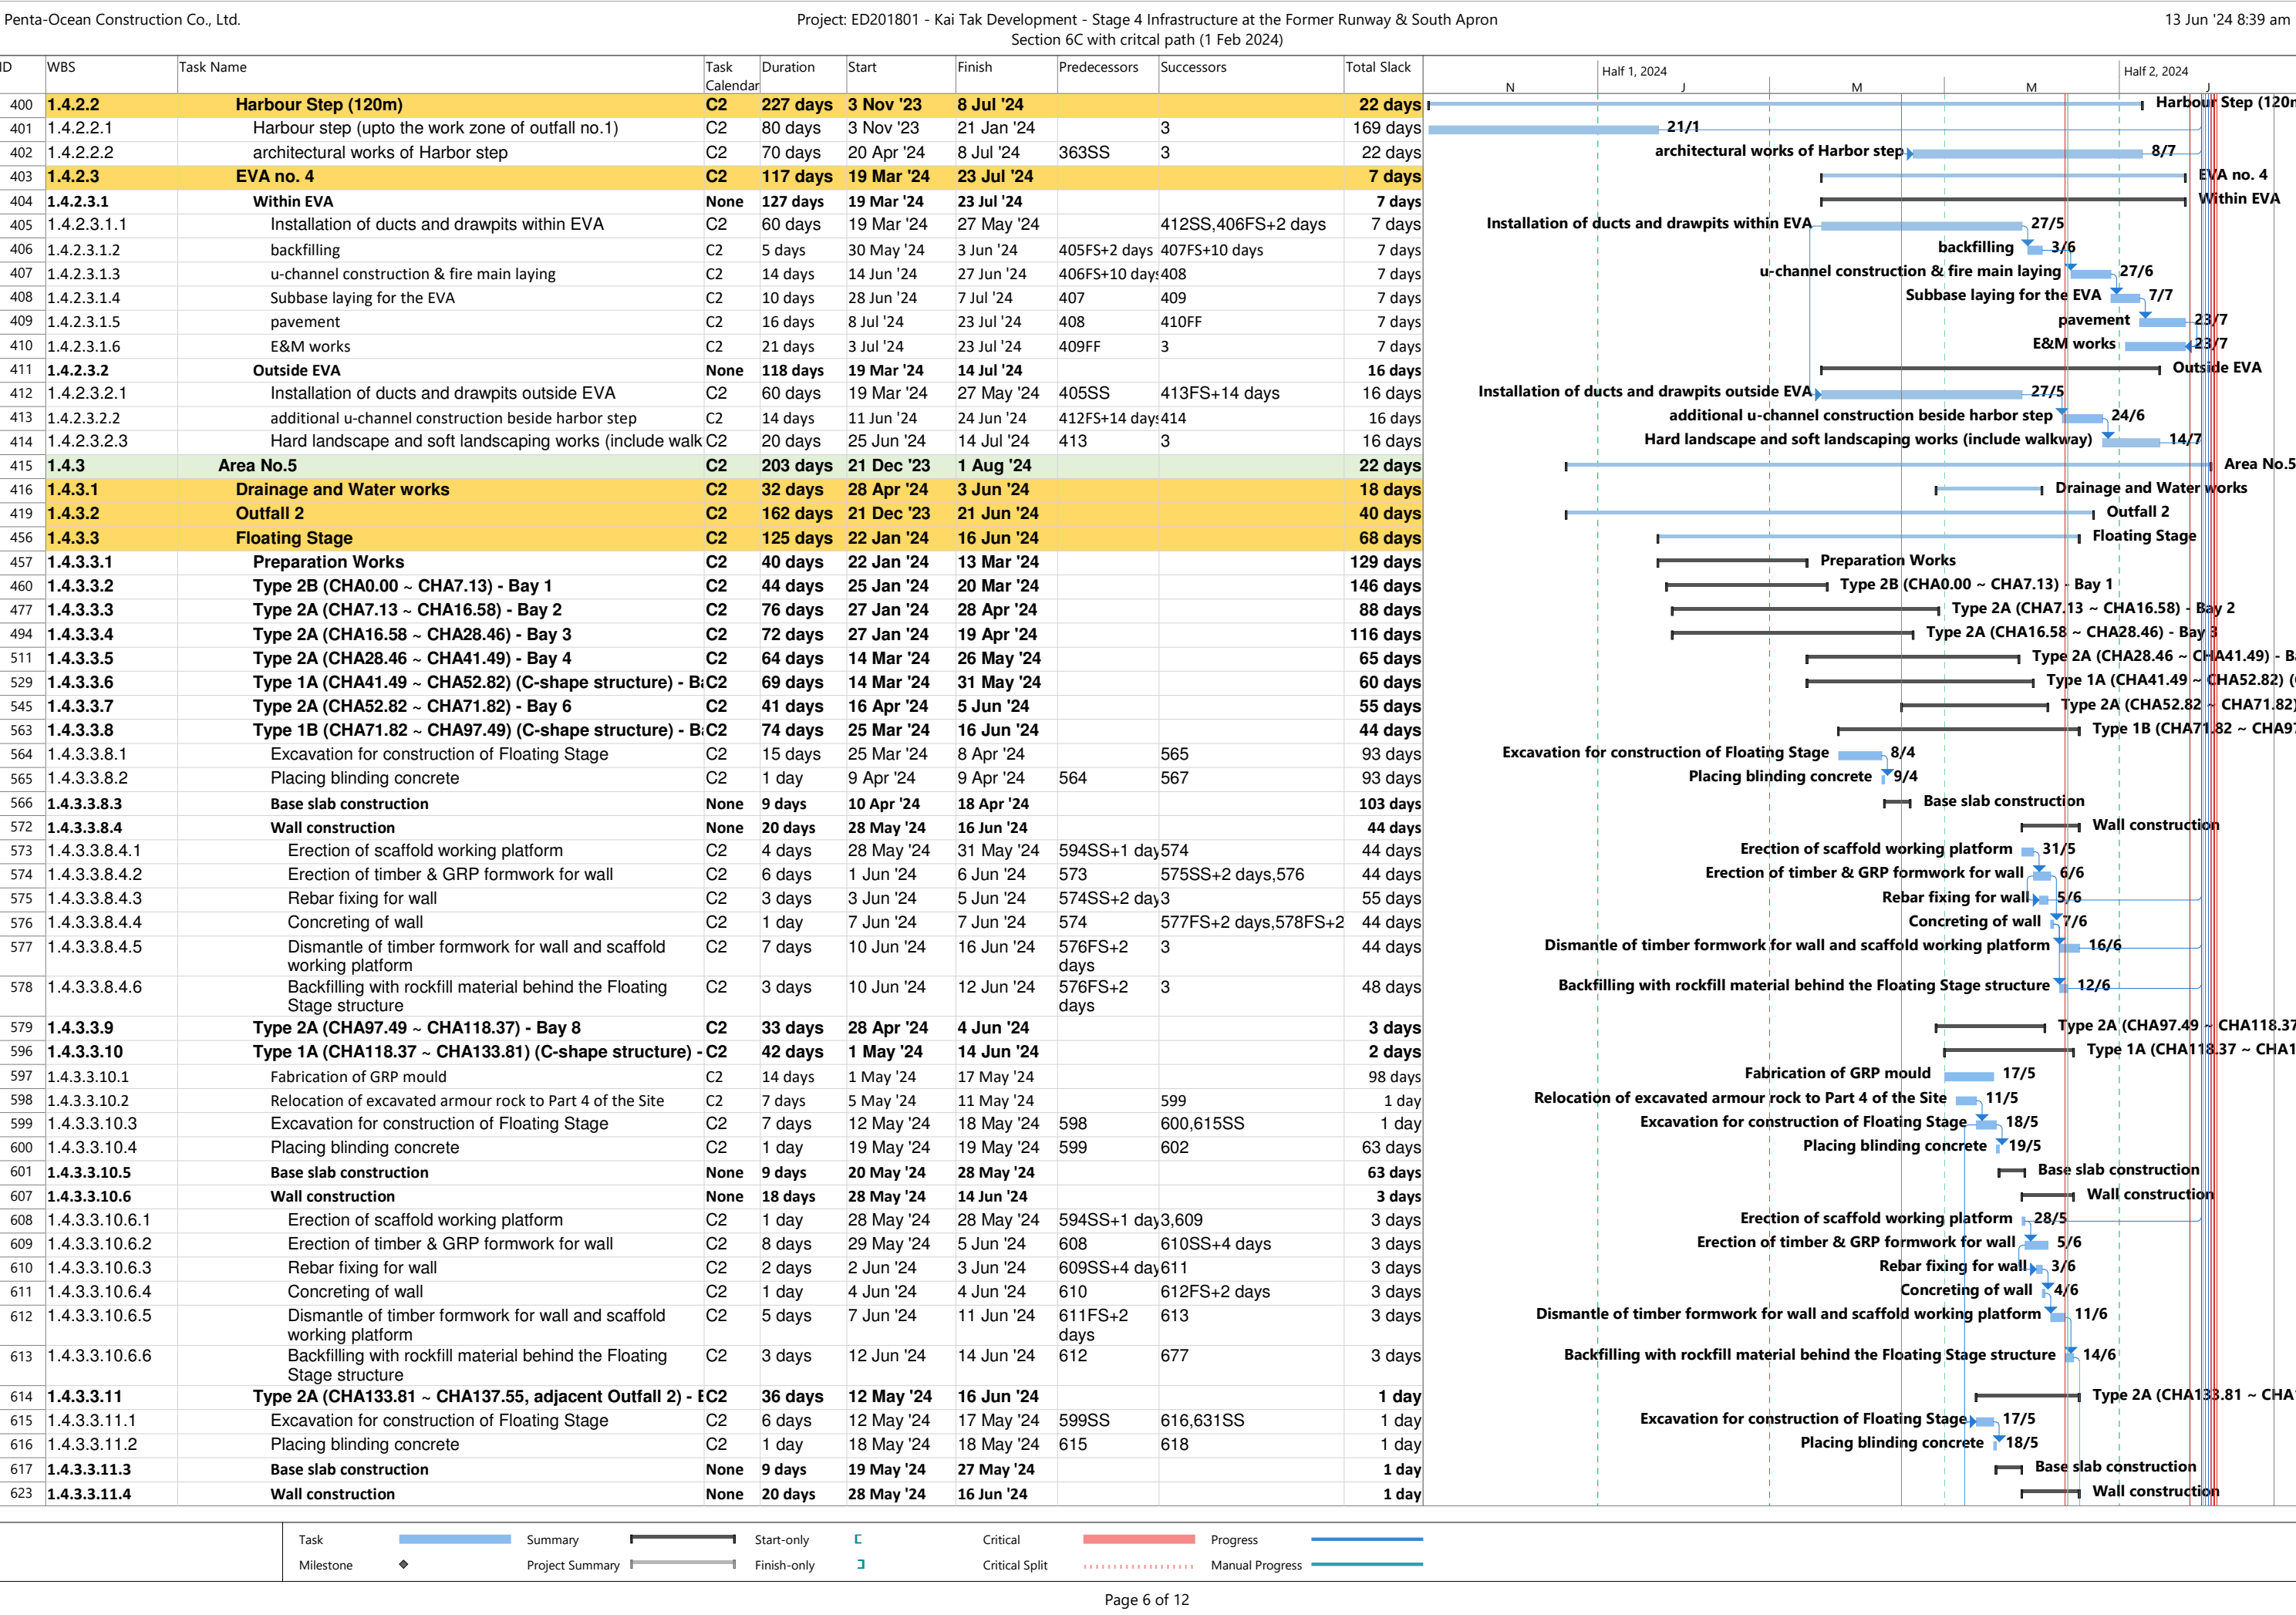

Task		Summary		Start-only		Critical		Progress	
Milestone		Project Summary		Finish-only		Critical Split		Manual Progress	

Task		Summary		Start-only		Critical		Progress	
Milestone		Project Summary		Finish-only		Critical Split		Manual Progress	

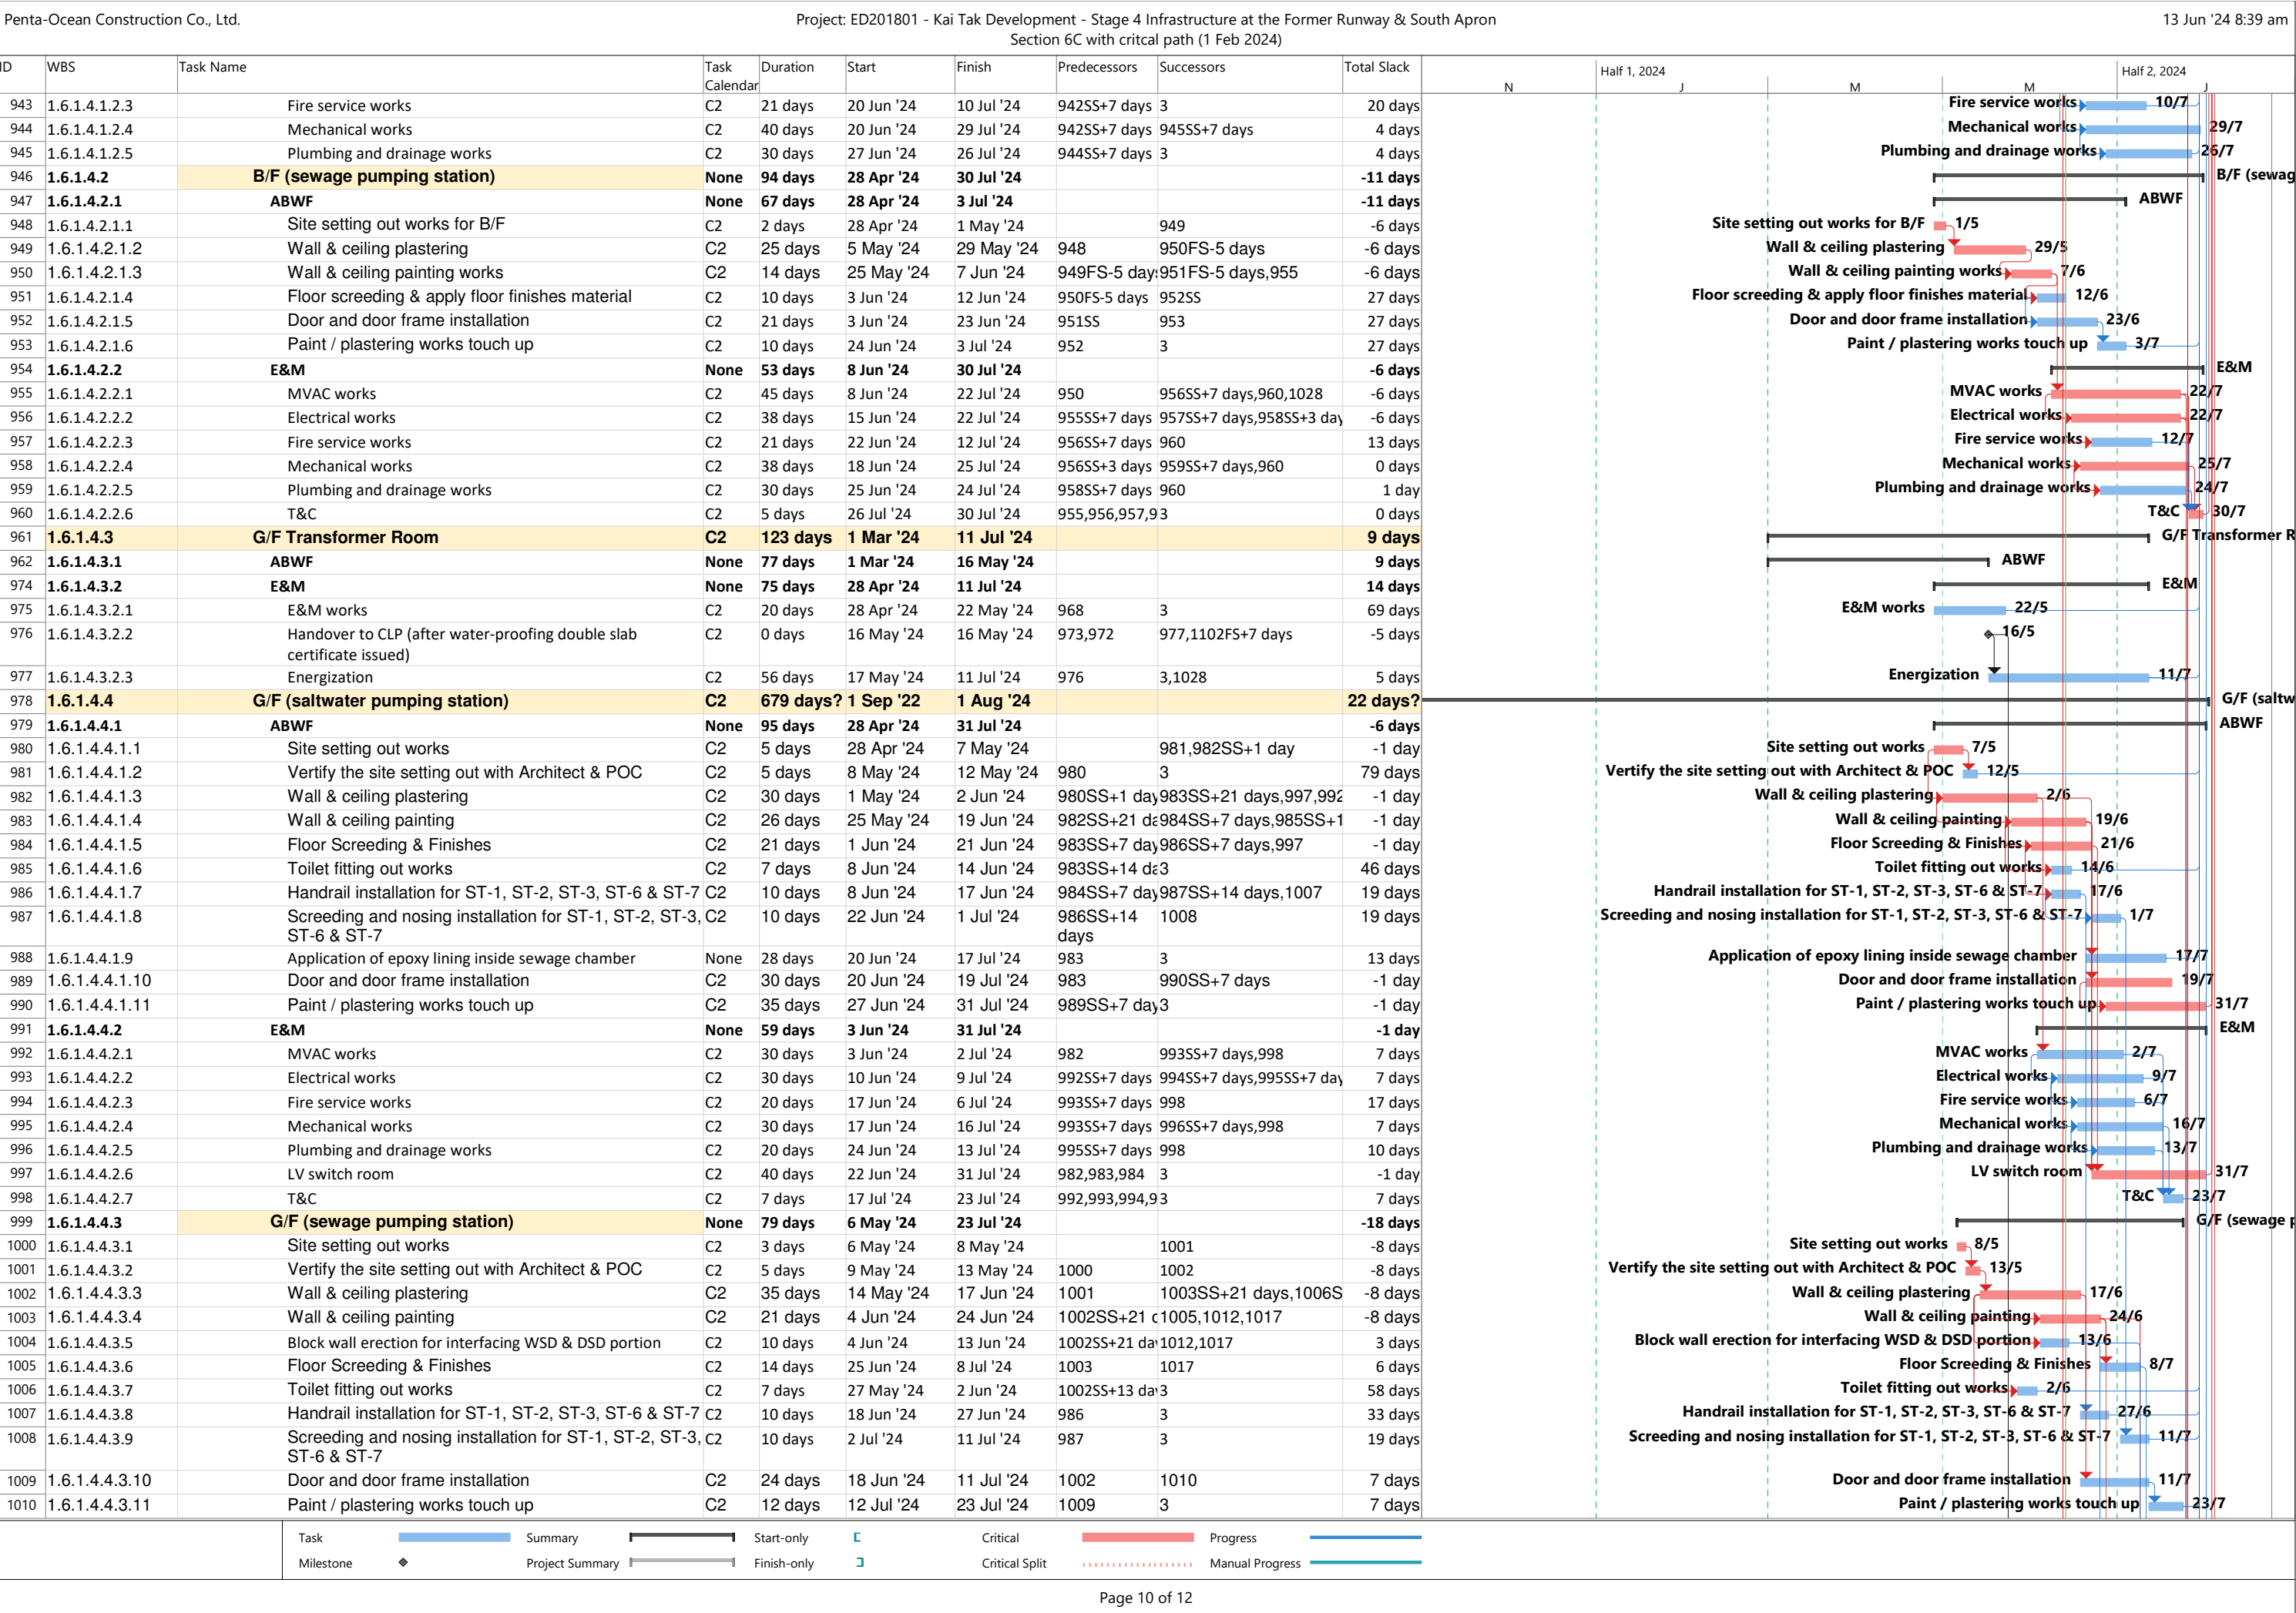

Appendix C – Apply permission for Environmental Monitoring

Propose alternative monitoring location: The Lok Sin Tong Modular Social Housing Scheme

Status: Rejected application

Email on: 10 May 2022

Subject **The Lok Sin Tong Benevolent Society Kowloon - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From

To

Bcc

Date 2022-05-10 15:48

- Figure 1 Impact dust measurement setup.jpg(~1.2 MB)
- Figure 2 Impact noise measurement setup.jpg(~979 KB)

Company: The Lok Sin Tong Benevolent Society Kowloon

By Email (

Dear Madam
5 May 2022

Dear Sir/ Madam,

Re: Environmental Monitoring for Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron

We, Ka Shing Management Consultant Limited (KS), is appointed by Civil Engineering and Development Department (CEDD), working as Environmental Team (ET) to conduct the monitoring and audit works as part of the EM&A programme of the Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron (KTD Stage 4 Project) starting from July 2019 to May 2024.

KTD Stage 4 project is located in the south-eastern part of Kowloon Peninsular of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. Your premise, Hong Kong Society for Blind Workshop and Hotels, is one of the proposed sensitive receivers.

We would like to obtain your kind permission for entering the premise to carry out baseline and impact monitoring, baseline dust monitoring (1-hour and 24-hour TSP monitoring) and baseline noise monitoring (30-minute) would need to conduct continuously for 14 days, our propose baseline monitoring date is June 2022.

After baseline monitoring, impact dust monitoring (1-hour and 24-hour TSP monitoring) and impact noise monitoring (30-minute) would take place between 08:00 hrs to 18:00 hrs in normal working days once every six days.

The monitoring location will be located on the roof top floor of The Lok Sin Tong Modular Social Housing Scheme at Junction of Sung Wong Toi Road and To Kwa Wan Road facing to Kai Tak Development area. 220V power supply is needed for 24-hour TSP monitor with size 0.5m (L) x 0.5m (W) x 1.4m (H). We will pay for the electricity. Similar setup photo records are shown in Figure 1 and Figure 2 for your kindly reference. Our technician will stay at the measurement point for 1-hour TSP and 30-minute noise measurement.

We hope to conduct site visit at 13:30 pm of 25 May 2022 (Wed).

Should you have any enquires regarding the measurement, please do not hesitate to contact [redacted] at [redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Email on: 13 October 2022

Subject **The Lok Sin Tong Benevolent Society Kowloon - Reject to Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From

To

Bcc

Date 2022-10-13 15:52

Company: The Lok Sin Tong Benevolent Society Kowloon

By Email [redacted]

Dear Sir/ [redacted]

Referring to the communication between your staff and me regarding the captioned work at 21 September 2022, the Lok Sin Tong Benevolent Society Kowloon was rejected the apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development. Due to electricity supply and security concern in Modular House, Environmental monitoring at Modular House is not allowed open.

Should you have any enquires regarding the measurement, please do not hesitate to contact [redacted] at [redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Propose alternative monitoring location: Freder Centre

Status: No reply from building management office unit the reporting month

Email on: 19 July 2022

Subject **Freder Centre - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From [Redacted]
To [Redacted]
Bcc [Redacted]

Date 2022-07-19 13:33

- Figure 1 Impact dust measurement setup.jpg(~1.2 MB)
- Figure 2 Impact noise measurement setup.jpg(~979 KB)

Company: Freder Centre

By Email [Redacted]
Dear Sir [Redacted]

Re: Environmental Monitoring for Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron

We, Ka Shing Management Consultant Limited (KS), is appointed by Civil Engineering and Development Department (CEDD), working as Environmental Team (ET) to conduct the monitoring and audit works as part of the EM&A programme of the Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron (KTD Stage 4 Project) starting from July 2019 to May 2024.

KTD Stage 4 project is located in the south-eastern part of Kowloon Peninsular of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. Your premise, Hong Kong Society for Blind Workshop and Hotels, is one of the proposed sensitive receivers.

We would like to obtain your kind permission for entering the premise to carry out baseline and impact monitoring, baseline dust monitoring (1-hour and 24-hour TSP monitoring) and baseline noise monitoring (30-minute) would need to conduct continuously for 14 days, our propose baseline monitoring date is August 2022.

After baseline monitoring, impact dust monitoring (1-hour and 24-hour TSP monitoring) and impact noise monitoring (30-minute) would take place between 08:00 hrs to 18:00 hrs in normal working days once every six days.

The monitoring location will be located on the roof top floor of Freder Centre at Junction of Sung Wong Toi Road and To Kwa Wan Road facing to Kai Tak Development area. 220V power supply is needed for 24-hour TSP monitor with size 0.5m (L) x 0.5m (W) x 1.4m (H). We will pay for the electricity. Similar setup photo records are shown in Figure 1 and Figure 2 for your kindly reference. Our technician will stay at the measurement point for 1-hour TSP and 30-minute noise measurement.

We hope to conduct site visit at 15:30pm of 26 July 2022 (Tue).

Should you have any enquires regarding the measurement, please do not hesitate to contact [Redacted] at [Redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Propose alternative monitoring location: New Port Centre
Status: No reply from building management office unit the reporting month

Email on: 19 July 2022

Subject **New Port Centre - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From [Redacted]
To [Redacted]
Bcc [Redacted]

Date 2022-07-19 13:33

- Figure 1 Impact dust measurement setup.jpg(~1.2 MB)
- Figure 2 Impact noise measurement setup.jpg(~979 KB)

Company: New Port Centre & Synergis management services limited

By Email [Redacted]

Dear Sir,

Re: Environmental Monitoring for Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron

We, Ka Shing Management Consultant Limited (KS), is appointed by Civil Engineering and Development Department (CEDD), working as Environmental Team (ET) to conduct the monitoring and audit works as part of the EM&A programme of the Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron (KTD Stage 4 Project) starting from July 2019 to May 2024.

KTD Stage 4 project is located in the south-eastern part of Kowloon Peninsular of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. Your premise, New Port Centre, is one of the proposed sensitive receivers.

We would like to obtain your kind permission for entering the premise to carry out baseline and impact monitoring, baseline dust monitoring (1-hour and 24-hour TSP monitoring) and baseline noise monitoring (30-minute) would need to conduct continuously for 14 days, our propose baseline monitoring date is August 2022.

After baseline monitoring, impact dust monitoring (1-hour and 24-hour TSP monitoring) and impact noise monitoring (30-minute) would take place between 08:00 hrs to 18:00 hrs in normal working days once every six days.

The monitoring location will be located on the roof top floor of New Port Centre at Junction of Sung Wong Toi Road and To Kwa Wan Road facing to Kai Tak Development area. 220V power supply is needed for 24-hour TSP monitor with size 0.5m (L) x 0.5m (W) x 1.4m (H). We will pay for the electricity. Similar setup photo records are shown in Figure 1 and Figure 2 for your kindly reference. Our technician will stay at the measurement point for 1-hour TSP and 30-minute noise measurement.

We hope to conduct site visit at 13:30pm of 26 July 2022 (Tue).

Should you have any enquires regarding the measurement, please do not hesitate to contact [Redacted] at [Redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Email on: 17 August 2022

Subject **Kum Shing Group and Hong Kong Energy Infrastructure Limited - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From [Redacted]
To [Redacted]
Bcc [Redacted]

Date 2022-08-17 11:54

- Figure 1 Impact dust measurement setup.jpg(~1.2 MB)
- Figure 2 Impact noise measurement setup.jpg(~979 KB)
- plug 01.jpg(~2.6 MB)

Company: Kum Shing Group and Hong Kong Energy Infrastructure Limited

By Email [Redacted]

Dear Sir,

Re: Environmental Monitoring for Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron

We, Ka Shing Management Consultant Limited (KS), is appointed by Civil Engineering and Development Department (CEDD), working as Environmental Team (ET) to conduct the monitoring and audit works as part of the EM&A programme of the Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron (KTD Stage 4 Project) starting from July 2019 to May 2024.

KTD Stage 4 project is located in the south-eastern part of Kowloon Peninsular of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. Your premise, New Port Centre, is one of the proposed sensitive receivers.

We would like to obtain your kind permission for entering the premise to carry out baseline and impact monitoring, baseline dust monitoring (1-hour and 24-hour TSP monitoring) and baseline noise monitoring (30-minute) would need to conduct continuously for 14 days, our propose baseline monitoring date is August 2022.

After baseline monitoring, impact dust monitoring (1-hour and 24-hour TSP monitoring) and impact noise monitoring (30-minute) would take place between 08:00 hrs to 18:00 hrs in normal working days once every six days.

The monitoring location will be located on the roof top floor of New Port Centre at Junction of Sung Wong Toi Road and To Kwa Wan Road facing to Kai Tak Development area. 220V power supply is needed for 24-hour TSP monitor with size 0.5m (L) x 0.5m (W) x 1.4m (H). We will pay for the electricity. Similar setup photo records are shown in Figure 1 and Figure 2 for your kindly reference. Our technician will stay at the measurement point for 1-hour TSP and 30-minute noise measurement.

We hope to loan the company on the roof top floor of Plug 01 for 24-hour TSP monitor of power supply.

Should you have any enquires regarding the measurement, please do not hesitate to contact [Redacted] at [Redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Propose alternative monitoring location: New Port Centre
Status: No reply from building management office unit the reporting month

Email on: 19 August 2022

Subject **RE: Kum Shing Group and Hong Kong Energy Infrastructure Limited - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From

To

Cc

Date 2022-08-19 08:36

Dear Mr. LEE,

As we do not have ownership to the roof, we'd suggest you to approach the management company of Newport Center for further discussion.

<https://www.synergis.com.hk/html/en/>

best,
Paul Lee

Email on: 15 September 2022

Subject **New Port Centre - Apply permission for Environmental Monitoring for Stage 4 of Kai Tak Development**



From

To

Bcc

Date 2022-09-15 15:35

- Figure 1 Impact dust measurement setup.jpg(~1.2 MB)
- Figure 2 Impact noise measurement setup.jpg(~979 KB)
- Figure 3 expect Impact dust measurement setup.png(~267 KB)
- Figure 4 power supply plug.jpg(~2.6 MB)

Company: New Port Centre & Synergis management services limited

By Email

Dear Sir,

Re: Environmental Monitoring for Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron

We, Ka Shing Management Consultant Limited (KS), is appointed by Civil Engineering and Development Department (CEDD), working as Environmental Team (ET) to conduct the monitoring and audit works as part of the EM&A programme of the Kai Tak Development - Stage 4 Infrastructure at the former runway and south apron (KTD Stage 4 Project) starting from July 2019 to May 2024.

KTD Stage 4 project is located in the south-eastern part of Kowloon Peninsular of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. Your premise, New Port Centre, is one of the proposed sensitive receivers.

We would like to obtain your kind permission for entering the premise to carry out baseline and impact monitoring, baseline dust monitoring (1-hour and 24-hour TSP monitoring) and baseline noise monitoring (30-minute) would need to conduct continuously for 14 days, our propose baseline monitoring date is August 2022.

After baseline monitoring, impact dust monitoring (1-hour and 24-hour TSP monitoring) and impact noise monitoring (30-minute) would take place between 08:00 hrs to 18:00 hrs in normal working days once every six days.

The monitoring location will be located on the roof top floor of New Port Centre at Junction of Sung Wong Toi Road and To Kwa Wan Road facing to Kai Tak Development area. 220V power supply is needed for 24-hour TSP monitor with size 0.5m (L) x 0.5m (W) x 1.4m (H). We will pay for the electricity. Similar setup photo records are shown in Figure 1 and Figure 2 for your kindly reference. The expect of impact dust measurement setup photo records are shown in Figure 3 and the power supply will come from the roof of the socket (Figure 4) for reference. Our technician will stay at the measurement point for 1-hour TSP and 30-minute noise measurement.

Should you have any enquires regarding the measurement, please do not hesitate to contact [redacted] at [redacted]

Thank you for your kind attention and I look forward to receiving your favourable reply soon.

Yours Sincerely,

Lee Wing Hang
Ka Shing Management Consultant Limited

Appendix D – Environmental monitoring schedules

Contract No. EDO 15/2018 Environmental Monitoring at Kai Tak Development Stage 4 Infrastructure at the former runway and south apron
Environmental Monitoring and Weekly Site Inspection Schedule for July 2024

July 2024

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4 Weekly Site Inspection	5 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	6
7	8	9 Weekly Site Inspection + SSMC meeting	10	11 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	12	13
14	15	16	17 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	18 Weekly Site Inspection	19	20
21	22	23 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	24	25 Weekly Site Inspection	26	27
28	29 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	30	31			

NOTE:

- 1) Site inspection schedule and Impact monitoring schedule may be changed due to unforeseen circumstance (e.g. adverse weather).
- 2) Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A) and M11), the premises owner rejected ET to conduct impact monitoring starting from 1 Sept 2022. No 24-TSP monitoring will be conducted at AM4(A) while 1-hr TSP at AM4(A) and 30-min noise monitoring at M11 will be conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for AM4(A) and M11 are confirmed.

Air Quality Monitoring Station

AM3 - Sky Tower

AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

AM7 - Hong Kong Children's Hospital

Noise Quality Monitoring Station

M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

M12 - Hong Kong Children's Hospital

Contract No. EDO 15/2018 Environmental Monitoring at Kai Tak Development Stage 4 Infrastructure at the former runway and south apron

Tentative Environmental Monitoring and Weekly Site Inspection Schedule for August 2023

August 2023

Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	2	3 Weekly Site Inspection	4	5
6	7 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	8 Weekly Site Inspection + SSMC meeting	9	10	11	12 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7
13	14	15	16	17 Weekly Site Inspection	18 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	19
20	21	22	23	24 Weekly Site Inspection 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	25	26
27	28	29	30 24-hr TSP: AM3, AM4(A), AM7 1-hr X3 TSP: AM3, AM4(A), AM7 30-min Noise: M11, M12	31 Weekly Site Inspection		

NOTE:

- 1) Site inspection schedule and Impact monitoring schedule may be changed due to unforeseen circumstance (e.g. adverse weather).
- 2) Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A) and M11), the premises owner rejected ET to conduct impact monitoring starting from 1 Sept 2022. No 24-TSP monitoring will be conducted at AM4(A) while 1-hr TSP at AM4(A) and 30-min noise monitoring at M11 will be conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for AM4(A) and M11 are confirmed.

Air Quality Monitoring Station

AM3 - Sky Tower

AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

AM7 - Hong Kong Children's Hospital

Noise Quality Monitoring Station

M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

M12 - Hong Kong Children's Hospital

Appendix E – Photographic records

Impact TSP Monitoring



Measurement setup at AM3



Measurement setup at AM4(A)




Measurement setup at AM7


Impact Noise Monitoring



Measurement setup at M11

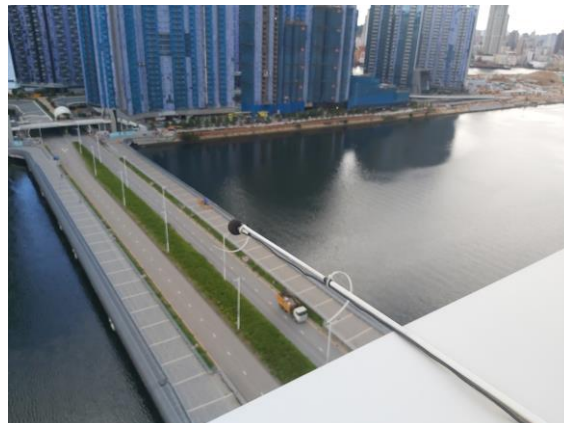

Measurement setup at M12

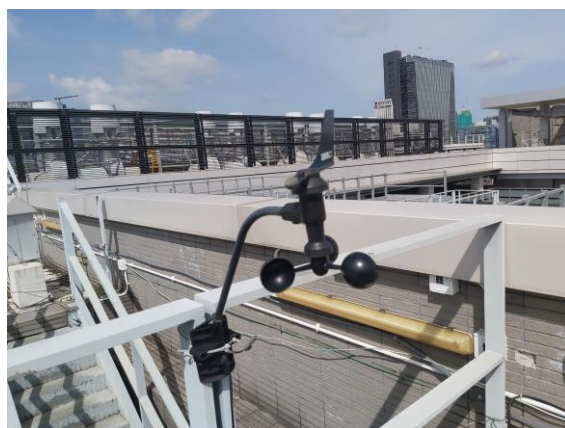

Weather Station at the rooftop of Hong Kong Children's Hospital

Appendix F – Calibration certificates, catalogue of air quality monitoring equipment

Catalogue of High Volume Sampler (HVS)



TSP MFC

Total Suspended Particulate, Mass Flow Controlled



MFC TSP

Ambient Air Sampler

The TE-5170 is a high volume ambient Total Suspended Particulate (TSP) air sampler featuring a mass flow controller (MFC) for accurate and consistent particulate sampling. The mass flow controller adjust the motor speed as the filter media collects particulate to maintain a constant flow rate throughout the entire sample duration. The system utilizes a stainless steel filter holder for use with standard 8" x 10" filter paper. The anodized aluminum shelter and robust electrical components allow the system to operate a continuous 24 hour sample.

ABOUT US: Tisch Environmental Inc. Tisch Environmental is the benchmark for high volume air sampling, particulate, metals, volatiles, and specialty monitoring equipment. Since the company's inception in 1953 as General Metal Works, our product line has expanded from the first high volume air sampler to include high-tech and custom samplers. Our clients are professionals from every sector of the regulatory and industrial markets.

Meets EPA CFR, Appendix B to Part 50

Total Suspended Particulate(TSP)

Mass Flow Controlled

7-Day Mechanical Timer

Elapsed Time Indicator

Aluminum Outdoor Shelter

Brush Style Motor

Dickson Chart Recorder, 24 Hour

Stainless Steel Filter Holder

36-60 CFM

Made In USA

Copyright © 2014 Tisch International All Rights Reserved
www.tischinternational.com



www.tisch-env.com

Tisch Environmental
145 S. Miami Ave
Cleveland, OH 44115
513-467-9000
sales@tisch-env.com



TSP MFC

MFC TSP Ambient Air Sampler

General System Specifications

Particulate Size:Total Suspended Particulate (TSP)

EPA Designation: CFR 40 Part 50 Appendix B

Flow Controller: Mass Flow Controller

Motor Style:Brush Style Motor Assembly

Pressure Recorder:Dickson Chart Recorder, 24 hour

Timer:7 Day Mechanical

Elapsed Time Indicator:Mechanical, Hours and Tenths

Flow Range:39-60CFM, 1.09M³M-1.68M³M

Housing:Anodized Aluminum

Filter Holder:Stainless Steel, 8" x 10"

4" Recorder Charts: Box of 100

Filter Holder: 8" x 10" Stainless Steel with hold down frame

Applications

US EPA Reference Method Sampling, CFR
Appendix J Part 50 Regulatory Compliance
Institutional Studies
Construction Sites
Bridge and Water Tower Painting Sites
Fence Line Monitoring
Industrial Monitoring
Landfill Monitoring
Public Health Applications

Optional Equipment

TE-3000 Filter Holder Cartridge
TE-G653 8" x 10" Glass Fiber Filter Media
TE-33384 Motor Brush Set (110volt)
TE-33378 Motor Brush Set (220volt)
TE-116311 Replacement Motor (110volt)
TE-116312 Replacement Motor (220volt)
TE-106 Recorder Charts
TE-160 Recorder Pen Points
TE-5018 Gasket 8" x 10"

Available Models

TE-5170 TSP MFC, 110 Volt 60 Hertz, 8 Amps

TE-5170X TSP MFC, 220 Volt 50 Hertz 4 Amps

TE-5170XZ TSP MFC, 220 Volts 60 Hertz, 4 Amps

Calibration Equipment

TE-5028 -Variable Flow Calibration Kit

TE-HVC-V Xcalibrator HiVol Calibrator

Physical Specifications

Weight: 75lbs, Shelter

Shipping Dimensions: 46"W x 23"L x 20" H, Shelter
19"W x 19"L x 20"H, Lid

Assembled Dimensions: 28"W x 28"L x 61"H

Copyright © 2014 Tisch International All Rights Reserved
www.tischinternational.com

www.tisch-env.com



Calibration Certificate of HVS

Air Sampler Calibration Curve Plotting & Calculation

(Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2024060701 Date of calibration : 07/06/2024

Location : Sky Tower Sampler : TE-5170X

Calibration Data

Ambient barometric pressure, Pa = 755.4 (mmHg) Ambient temperature, Ta = 299.75 (deg K)


Qstd Slope, m = 2.03976 Qstd Intercept, b = -0.012990

Calibration Curve

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	8.00	1.385	50.0	49.70
13	6.50	1.249	45.0	44.73
10	4.40	1.029	38.0	37.77
7	3.30	0.892	33.0	32.80
5	2.40	0.761	27.0	26.84

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1 / m \left[(I) \left(\sqrt{\left(P_{atm} / 760 \right) \left(298 / T_{atm} \right)} \right) - b \right]$	35.732	0.3774	0.9980

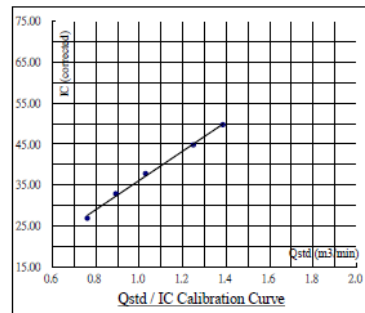

Calibration curve requirements : (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³ / min).

Remark : $Qstd (m^3/min) = 1/m \left[\sqrt{\left(H_2O (Pa / 760) \right) \left(298 / T_a \right)} - b \right]$

$IC (corrected) = I \left[\sqrt{\left(Pa / 760 \right) \left(298 / Ta \right)} \right]$

$FLOW (corrected) = \sqrt{\left(FLOW (mano) \right) \left(Pa / 760 \right) \left(298 / Ta \right)}$

Calibrated by : Poon Tsz Wing

Name : (Poon Tsz Wing)

Checked by : Choy Ching Yee

Name : (Choy Ching Yee)

Form No. DHS-HVS-CAL-01 16 01 2020

Air Sampler Calibration Curve Plotting & Calculation

(Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2024060703 Date of calibration : 07/06/2024

Location : Hong Kong Children's Hospital Sampler : TE-5170X

Calibration Data

Ambient barometric pressure, Pa = 755.4 (mmHg) Ambient temperature, Ta = 299.75 (deg K)


Qstd Slope, m = 2.03976 Qstd Intercept, b = -0.012990

Calibration Curve

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	7.90	1.376	50.0	49.70
13	6.80	1.277	44.0	43.74
10	4.60	1.052	37.0	36.78
7	3.30	0.892	32.0	31.81
5	2.20	0.729	26.0	25.85

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1 / m \left[(I) \left(\sqrt{\left(P_{atm} / 760 \right) \left(298 / T_{atm} \right)} \right) - b \right]$	35.218	0.0617	0.9954

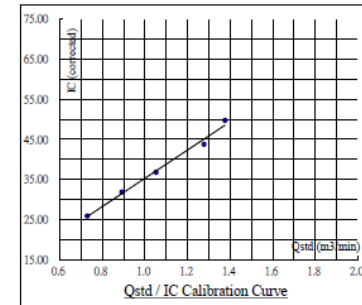

Calibration curve requirements : (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³ / min).

Remark : $Qstd (m^3/min) = 1/m \left[\sqrt{\left(H_2O (Pa / 760) \right) \left(298 / T_a \right)} - b \right]$

$IC (corrected) = I \left[\sqrt{\left(Pa / 760 \right) \left(298 / Ta \right)} \right]$

$FLOW (corrected) = \sqrt{\left(FLOW (mano) \right) \left(Pa / 760 \right) \left(298 / Ta \right)}$

Calibrated by : Poon Tsz Wing

Name : (Poon Tsz Wing)

Checked by : Choy Ching Yee

Name : (Choy Ching Yee)

Form No. DHS-HVS-CAL-01 16 01 2020

Calibration Certificate of HVS

Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2024053001 Date of calibration : 30/05/2024

Model no : GS2310 Serial number : 10346

Calibration Data

Ambient barometric pressure, Pa = 753.9 (mmHg) Ambient temperature, Ta = 298.65 (deg K)


Qstd Slope, m = 2.03976 Qstd Intercept, b = -0.012990

Calibration Curve

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	7.60	1.351	50.0	49.74
13	6.50	1.250	44.0	43.77
10	4.40	1.029	38.0	37.81
7	3.20	0.879	32.0	31.84
5	2.20	0.730	27.0	26.86

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff, r
Dickson recorder	$Q_{std} = 1/\text{ml} \left[(I) \left(\sqrt{\left(\frac{P_{av}}{760} \right) \left(\frac{298}{T_{av}} \right)} \right) - b \right]$	35.445	0.8648	0.9952

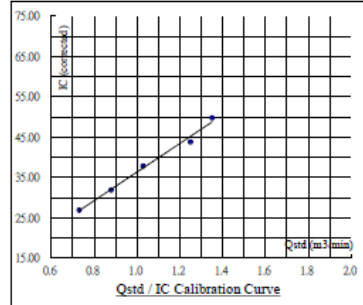

Calibration curve requirements : (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³/min).

Remark : $Q_{std} \text{ (m}^3/\text{min)} = 1/\text{ml} \left[\sqrt{\left(\frac{H_2O}{Pa} \right) \left(\frac{298}{Ta} \right)} \right] - b$.

IC (corrected) = $I \left[\sqrt{\left(\frac{Pa}{760} \right) \left(\frac{298}{Ta} \right)} \right]$.

FLOW (corrected) = $\sqrt{\left(\frac{FLOW \text{ (mano)}}{Pa} \right) \left(\frac{298}{Ta} \right)}$.

Calibrated by : Poon Tsz Wing Checked by : Choy Ching Yee

Form No. BNS-IVS-CAL-04 16/01/2020

Orifice Transfer Standard Certification Worksheet TE-5025A



RECALIBRATION
DUE DATE:
May 6, 2025

Certificate of Calibration

Calibration Certification Information			
Cal. Date: May 6, 2024	Rootmeter S/N: 438320	Ta: 295 °K	
Operator: Jim Tisch		Pa: 748.5 mm Hg	
Calibration Model #: TE-5025A	Calibrator S/N: 0006		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4190	3.2	2.00
2	3	4	1	1.0030	6.4	4.00
3	5	6	1	0.8950	7.9	5.00
4	7	8	1	0.8520	8.8	5.50
5	9	10	1	0.7040	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9907	0.6982	1.4106	0.9957	0.7017	0.8878
0.9864	0.9835	1.9949	0.9914	0.9885	1.2556
0.9844	1.0999	2.2304	0.9894	1.1055	1.4037
0.9832	1.1540	2.3393	0.9882	1.1599	1.4723
0.9781	1.3893	2.8213	0.9830	1.3964	1.7756
QSTD		m= 2.03976 b= -0.01299 r= 1.00000	QA		
			m= 1.27726 b= -0.00818 r= 1.00000		

Calculations			
$V_{std} = \Delta Vol \left(\frac{Pa - \Delta P}{P_{std}} \right) \left(\frac{T_{std}}{Ta} \right)$	$V_a = \Delta Vol \left(\frac{Pa - \Delta P}{Pa} \right)$		
$Q_{std} = V_{std} / \Delta Time$	$Q_a = V_a / \Delta Time$		
For subsequent flow rate calculations:			
$Q_{std} = 1/\text{ml} \left(\sqrt{\Delta H \left(\frac{Pa}{P_{std}} \right) \left(\frac{T_{std}}{Ta} \right)} - b \right)$	$Q_a = 1/\text{ml} \left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} - b \right)$		

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH:	calibrator manometer reading (in H2O)
ΔP:	rootsmeter manometer reading (mm Hg)
Ta:	actual absolute temperature (°K)
Pa:	actual barometric pressure (mm Hg)
b:	intercept
m:	slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
145 South Miami Avenue
Village of Cleves, OH 45002

www.tisch-env.com
TOLL FREE: (877)263-7610
FAX: (513)467-9009

Catalogue of Dust Meter (TSI Sidepak AM510)

The SidePak AM510 monitor's easy-to-read display shows your data as both real-time aerosol mass-concentration and 8-hour time-weighted average (TWA). With its convenient data logging and long battery life, the AMS10 is also ideal for extended sampling. The easy-to-use TrakPro Data Analysis Software lets you create effective graphs and reports.

User Friendly

- + Small, lightweight and quiet to maximize worker acceptance
- + Rugged design with secure belt clip
- + Easy-to-understand user interface with only four keys
- + Lockable keypad prevents tampering while sampling
- + User-adjustable sample flow rate
- + Define, label and store multiple calibration constants
- + Easy-to-read LCD display
- + Convenient, threaded tripod socket accommodates area sampling

Advanced Features

- + Smart Battery Management System provides precise run time information, maximizes battery capacity and speeds charging
- + Integrated pump allows use of size-selective aerosol inlet conditioners
- + Built-in impactors let you choose "none," 1.0, 2.5 or 10-micron cut off
- + 10-mm Dorr-Oliver cyclone for respirable sampling
- + Display shows real-time concentrations (mg/m³) and "on-the-fly" TWA as you data log
- + Display statistics: max, min and average readings, elapsed time and 8-hour TWA

Quick and Easy Reports

- + Convenient preprogramming for occupational exposure sampling
- + Data log for long periods and store multiple tests
- + Analyze data, print graphs and create reports with TrakPro Data Analysis Software
- + USB port lets you conveniently connect to your computer

Power to Spare

- + Long-lasting NiMH rechargeable battery packs eliminate "memory" issues
- + Choice of rechargeable NiMH smart battery packs or AA-cell pack

Model AM510 SidePak Personal Aerosol Monitor

Sensitivity	
Sensor Type	90° light scattering, 670 nm laser diode
Aerosol Concentration Range	0.001 to 20 mg/m ³ (calibrated to respirable fraction of ISO 12103-1, A1 test dust)
Particle Size Range	0.1 to 10 micrometer (µm)
Minimum Resolution	0.001 mg/m ³
Zero stability	±0.001 mg/m ³ over 24 hours using 10-second time-constant
Temperature Coefficient	Approximately +0.0005 mg/m ³ per °C (for variations from temperature at which instrument was last zeroed)
Flow Rate	
Range	User-adjustable, 0.7 to 1.8 liters/min (L/min)
Temperature Range	
Operating Range	32 to 120°F (0 to 50°C)
Storage Range	-4 to 140°F (-20 to 60°C)
Operational Humidity	0 to 95% RH, non-condensing
Time Constant (LCD display)	
Range	User-adjustable, 1 to 60 seconds
Data Logging	
Data Points	Approx. 31,000
Logging Interval	User-adjustable, 1 second to 1 hour
User-Select Calibration Factors	
Factory Setting	1.0 (non-adjustable)
User-defined Settings	3, with user-defined labels
Range	0.1 to 10.0, user-adjustable
Physical	
External Dimensions	4.2 x 3.7 x 2.8 in. (106 x 92 x 70 mm) with 801723, 801724, 801729 or 801743 battery
	5.1 x 3.7 x 2.8 in. (130 x 92 x 70 mm) with 801708, 801722, 801728, 801735, or 801736 battery
Weight	16 oz (0.46 kg) with 801723, 801724, 801729 or 801743 battery
	19 oz (0.54 kg) with 801708, 01722, 801728, 801735, or 801736 battery
Display	2 line x 12 character LCD
Tripod Socket	1/4"-20 female thread
Power Supply/Charger (P/N 2613210)	
Input Voltage Range	100 to 240 VAC, 50 to 60 Hz
Output Voltage	9 VDC @ 1.0 A

Maintenance

Factory Clean/Calibrate	Recommended annually
User Zero Calibration	Before each use
User Flow Calibration	As needed

Communications Interface

Type	USB 1.1
Connector, Instrument	USB Mini-B (socket)

Minimum Computer Requirements for TrakPro™ Data Analysis Software

Communications Port	Universal Serial Bus (USB) v 1.1 or higher
Operating System	Microsoft Windows® XP, or 7 (32-bit or 64-bit) operating systems

Battery Performance

Battery Options	Charge Time (hrs)*	Intrinsic Safety Rating	Run Time (hrs @ 1.7 L/min)
1600 mAh NiMH Pack, 4.8 V (P/N 801723)	3.0	No	7.1
1650 mAh NiMH Pack, 4.8V (P/N 801724, 801729 or 801743)	3.5	CSA**	7.5
2700 mAh NiMH Pack, 4.8 V (P/N 801722 or 801728)	5.5	No	12.0
2700 mAh NiMH Pack, 4.8 V (P/N 801735)	5.5	No	12.0
6-Cell AA-size Alkaline Pack*** (P/N 801708 or 801736 with six user-supplied AA cells)	N/A	No	22.5

*Of a fully depleted battery

**All dust plugs and dust gaskets must be installed.

***Using Energizer AA-size, E91 alkaline batteries.

Battery Level Indicator

The Smart Battery Management System™ technology utilizes a built-in "gauge" in the SidePak™ battery packs. The gauge monitors battery capacity and calculates run time information by dividing capacity of the battery (mAh) by the instantaneous current consumed by the instrument (mA). This calculation is correct for current operating conditions and can change due to current (mA) consumption or changes in battery capacity.



Calibration Certificate of Dust Meter (TSI Sidepak AM510)

CERTIFICATE OF CALIBRATION AND TESTING TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com																				
Environment Conditions <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>Temperature</td> <td>74.14 (23.4)</td> <td>°F (°C)</td> </tr> <tr> <td>Relative Humidity</td> <td>47.6</td> <td>%RH</td> </tr> <tr> <td>Barometric Pressure</td> <td>28.96 (980.7)</td> <td>inHg (hPa)</td> </tr> </table>				Temperature	74.14 (23.4)	°F (°C)	Relative Humidity	47.6	%RH	Barometric Pressure	28.96 (980.7)	inHg (hPa)	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>Model</td> <td>AM510</td> </tr> <tr> <td>Serial Number</td> <td>11208032</td> </tr> </table>				Model	AM510	Serial Number	11208032
Temperature	74.14 (23.4)	°F (°C)																		
Relative Humidity	47.6	%RH																		
Barometric Pressure	28.96 (980.7)	inHg (hPa)																		
Model	AM510																			
Serial Number	11208032																			
☐ As Left ☐ In Tolerance ☒ As Found ☒ Out of Tolerance																				
Concentration Linearity Plot 																				
System ID: DT1101-02																				
CONCENTRATION Unit: mg/m³																				
#	STANDARD	MEASURED	ALLOWABLE RANGE	#	STANDARD	MEASURED	ALLOWABLE RANGE													
1	1.205	1.108	1.084-1.326	3	0.041	* 0.059	0.029-0.053													
2	0.150	0.156	0.128-0.172	4	11.824	10.777	10.642-13.006													
TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass per standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 4:1																				
Measurement Variable DC Voltage E010539 12-05-22 06-30-24 Microbalance M001324 01-09-23 01-31-25 Flowmeter E002471 05-22-23 05-31-24		Measurement Variable Photometer E003433 03-21-23 09-30-23 Pressure E003511 10-25-22 10-31-23 DC Voltage E003315 01-09-23 01-31-24																		
 Verified				August 8, 2023 Date																

Personal Aerosol Monitor Performance check with High Volume Sampler

Performance Check ref. No. AS0240523-1 Report Issue Date 23/05/2024
Date of performance check 23/05/2024

Objective:


A dust meter and a Total Suspended Particulate High Volume Air Sampler (HVS) were placed together to measure the Total Suspended Particulate (TSP) concentrations simultaneously to check the performance.

Equipment Used:

Equipment	Manufacturer and Model	Serial Number
Personal Aerosol Monitor	TSI AM510 Sidepak	11208032
Total Suspended Particulate High Volume Air Sampler	GS2310	10346

Results:

Equipment	Measurement Result, $\mu\text{g}/\text{m}^3$			
TSI AM510 Sidepak	64	142	224	336
High Volume Air Sampler (HVS)	41	116	181	267

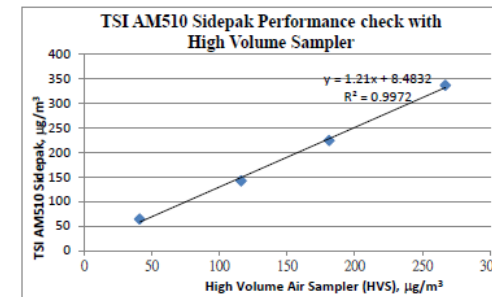

Tested by: P # Checked by: C
Name: (Poon Tsz Wing) Name: (Choy Ching Yee)

Form No. ENV CAL SAMPLER CCI 441212/2003

Calibration Certificate of Dust Meter (TSI Sidepak AM510)

CERTIFICATE OF CALIBRATION AND TESTING TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com																				
Environment Conditions <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>Temperature</td> <td>73.99 (23.3)</td> <td>*F (°C)</td> </tr> <tr> <td>Relative Humidity</td> <td>51.8</td> <td>%RH</td> </tr> <tr> <td>Barometric Pressure</td> <td>28.83 (976.3)</td> <td>inHg (hPa)</td> </tr> </table>				Temperature	73.99 (23.3)	*F (°C)	Relative Humidity	51.8	%RH	Barometric Pressure	28.83 (976.3)	inHg (hPa)	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>Model</td> <td>AM510</td> </tr> <tr> <td>Serial Number</td> <td>11411017</td> </tr> </table>				Model	AM510	Serial Number	11411017
Temperature	73.99 (23.3)	*F (°C)																		
Relative Humidity	51.8	%RH																		
Barometric Pressure	28.83 (976.3)	inHg (hPa)																		
Model	AM510																			
Serial Number	11411017																			
☒ As Left ☒ In Tolerance ☐ As Found ☐ Out of Tolerance																				
Concentration Linearity Plot 																				
System ID: DT1101-01																				
CONCENTRATION Unit: mg/m³																				
#	STANDARD	MEASURED	ALLOWABLE RANGE	#	STANDARD	MEASURED	ALLOWABLE RANGE													
1	1.612	1.529	1.451-1.773	3	0.074	0.075	0.052-0.096													
2	0.242	0.234	0.206-0.278	4	15.040	14.957	13.536-16.544													
TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass per standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 4:1.																				
Measurement Variable Photometer DC Voltage(Keithley) Pressure		System ID E003319 E002455 E005651		Last Cal. 03-17-23 06-13-23 07-24-23		Cal. Due 09-30-23 06-30-24 07-31-24														
Measurement Variable Flowmeter Microbalance		System ID E004570 M001324		Last Cal. 06-05-23 02-09-23		Cal. Due 06-30-24 02-28-25														
 Calibrated				August 9, 2023 Date																

Personal Aerosol Monitor Performance check with High Volume Sampler

Performance Check ref. No. AS0240523-3 Report Issue Date 23/05/2024
Date of performance check 23/05/2024

Objective:


A dust meter and a Total Suspended Particulate High Volume Air Sampler (HVS) were placed together to measure the Total Suspended Particulate (TSP) concentrations simultaneously to check the performance.

Equipment Used:

Equipment	Manufacturer and Model	Serial Number
Personal Aerosol Monitor	TSI AM510 Sidepak	11411017
Total Suspended Particulate High Volume Air Sampler	GS2310	10346

Result:

Equipment	Measurement Result, $\mu\text{g}/\text{m}^3$			
TSI AM510 Sidepak	60	143	213	337
High Volume Air Sampler (HVS)	41	116	181	267

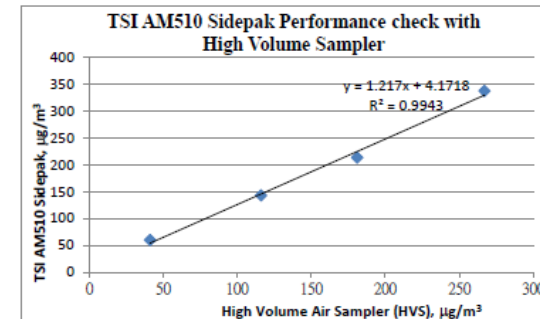

Tested by: Poon Tsz Wing Checked by: Choy Ching Yee
Name: (Poon Tsz Wing) Name: (Choy Ching Yee)

Form No. ENV CAL SAMPLER CCI 4412/12/2003

Catalogue of Weather Station

Cabled Vantage Pro2™ & Vantage Pro2 Plus™ Stations



**6152C
6162C**

Vantage Pro2™

The Vantage Pro2™ (# 6152C) and Vantage Pro2™ Plus (# 6162C) cabled weather stations include two components: the Integrated Sensor Suite (ISS) and the console. The ISS contains the sensor interface module (SIM), rain collector, an anemometer, and a passive radiation shield. The Vantage Pro2 console provides the user interface, data display, and calculations. The Vantage Pro2 Plus weather station includes two additional sensors that are optional on the Vantage Pro2 and purchased separately: the UV Sensor and the Solar Radiation Sensor. The console and ISS are powered by an AC-power adapter connected to the console. Batteries can be installed in the console to provide a backup power supply. Use WeatherLink® to let your weather station interface with a computer, log data, and upload weather information to the Internet. The 6152C and 6162C models rely on passive shielding to reduce solar-radiation induced temperature errors in the outside temperature sensor readings.

Integrated Sensor Suite (ISS)

Operating Temperature	-40° to +150°F (-40° to +65°C)
Non-operating Temperature	-40° to +158°F (-40° to +70°C)
Current Draw	5 mA (average) at 4 to 6 VDC for ISS only. 10 mA average for both console and ISS
Connectors, Sensor	Modular RJ-11
Cable Type	4-conductor, 26 AWG
Cable Length, Anemometer	40' (12 m) (included); 240' (73 m) (maximum recommended)

Note: Maximum displayable wind decreases as the length of cable increases. At 140' (42 m) of cable, the maximum wind speed displayed is 135 mph (60 m/s); at 240' (73 m), the maximum wind speed displayed is 100 mph (34 m/s).

Wind Speed Sensor	Solid state magnetic sensor
Wind Direction Sensor	Wind vane with potentiometer
Rain Collector Type	Tipping bucket, 0.01" per tip (0.2 mm with metric rain adapter), 33.2 in ² (214 cm ²) collection area
Temperature Sensor Type	PN Junction Silicon Diode
Relative Humidity Sensor Type	Film capacitor element
Housing Material	UV-resistant ABS, polypropylene
Sensor Inputs	
RF Filtering	RC low-pass filter on each signal line

ISS Dimensions(not including anemometer or bird spikes):

Vantage Pro2 with Standard Rad Shield	14.0" x 9.4" x 14.5" (356 mm x 239 mm x 368 mm)
Vantage Pro2 with Fan-Aspirated Rad Shield	20.8" x 9.4" x 16.0" (528 mm x 239 mm x 406 mm)
Vantage Pro2 Plus with Standard Rad Shield	14.3" x 9.7" x 14.5" (363 mm x 246 mm x 368 mm)
Vantage Pro2 Plus with Fan-Aspirated Rad Shield	21.1" x 9.7" x 16.0" (536 mm x 246 mm x 406 mm)

DAVIS  **Davis Instruments** 3465 Diablo Ave., Hayward, CA 94545-2778 USA
(510) 732-9229 • FAX (510) 670-0589 • sales@davisinstruments.com • www.davisinstruments.com

DS6152C, 6162C Rev. W 12/7/18
1

7
Vantage Pro2™

Ultra Violet (UV) Radiation Index (requires UV sensor)

Resolution and Units	0.1 Index
Range	0 to 16 Index
Accuracy	±5% of full scale (Reference: Yankee UVB-1 at UV index 10 (Extremely High))
Cosine Response	±4% FS (0° to 90° zenith angle)
Update Interval	50 seconds to 1 minute (5 minutes when dark)
Current Graph Data	Instant Reading and Hourly Average; Daily, Monthly High
Historical Graph Data	Hourly Average, Daily, Monthly Highs
Alarm	High Threshold from Instant Calculation

Wind

Wind Chill (Calculated)	
Resolution and Units	1°F or 1°C (user-selectable); °C is converted from °F and rounded to the nearest 1°C
Range	-110° to +135°F (-79° to +57°C)
Accuracy	±2°F (±1°C) (typical)
Update Interval	10 to 12 seconds
Source	United States National Weather Service (NWS)/NOAA
Equation Used	Osczevski (1995) (adopted by US NWS in 2001)
Variables Used	Instant Outside Temperature and 10-min. Avg. Wind Speed
Current Display Data	Instant Calculation
Current Graph Data	Instant Calculation; Hourly, Daily and Monthly Low
Historical Graph Data	Hourly, Daily and Monthly Lows
Alarm	Low Threshold from Instant Calculation

Wind Direction

Range	1 - 360°
Display Resolution	16 points (22.5°) on compass rose, 1° in numeric display
Accuracy	±3°
Update Interval	2.5 to 3 seconds
Current Graph Data	Instant Reading (user adjustable); 10-min. Dominant; Hourly, Daily, Monthly Dominant
Historical Graph Data	Past 6 10-min. Dominants on compass rose only; Hourly, Daily, Monthly Dominants

Wind Speed

Resolution and Units	1 mph, 1 km/h, 0.4 m/s, or 1 knot (user-selectable) Measured in mph; other units are converted from mph and rounded to nearest 1 km/hr, 0.1 m/s, or 1 knot.
Range	0 to 200 mph, 0 to 173 knots, 0 to 89 m/s, 0 to 322 km/h
Update Interval	Instant Reading: 2.5 to 3 seconds, 10-minute Average: 1 minute
Accuracy	±2 mph (2 kts, 3.2 km/h, 0.9 m/s) or ±5%, whichever is greater
Maximum Cable Length	540' (165 m) (Note that maximum wind speed reading decreases as length of cable from anemometer to ISS increases.)
Current Display Data	Instant
Current Graph Data	Instant Reading; 10-minute and Hourly Average; Hourly High; Daily, Monthly and Yearly High with Direction of High
Historical Graph Data	10-min. and Hourly Averages; Hourly Highs; Daily, Monthly and Yearly Highs with Direction of Highs
Alarms	High Thresholds from Instant Reading and 10-minute Average

Calibration Certificate of Weather Station



Cal Lab Limited 校正實驗室有限公司

Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
Tsuen Wan, N.T., Hong Kong
Tel: +852 25680106 Email: info@callab.com.hk
Fax: +852 30116194 Website: www.callab.com.hk

Calibration Certificate No.: CC0122402

Customer Information

Customer: Castco Testing Centre Limited
Address: 33, On Kui Street, Fanling, N.T.

Equipment Identification

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.:
Weather Station	Davis	Vantage PRO 2	BD190307008	AAST-WS-O-1

Certificate Information


Date of Receipt:	6 February 2024	Calibration Condition:	21.5°C, 55%RH, 1012hPa
Date of Calibration:	16 February 2024	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	JJF 1183-2007, JJF 1076-2001, SOP-116	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Platinum resistance thermometer	KPPRHT-A-1	KCI I-1095, KCI P-1095	9 November 2024
Humidity sensor	KPPRHT-A-1	KCI I-1095, KCI P-1095	9 November 2024
Hot Wire Anemometer	9535	T95351316004	11 August 2024

Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.

Approved By:


Warren Yeung

Company Chop:



Certificate Issue Date: 16 February 2024

CT-BEG-04

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
- The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0122402
Page 1 of 2

Appendix G – Weather information

General Information

Date	Absolute Daily Min Temperature (°C)	Absolute Daily Max Temperature (°C)	Total Rainfall (mm)
01/07/2024	29.3	32.4	2.5
02/07/2024	29.1	32.7	5.3
03/07/2024	28.7	33.6	0
04/07/2024	27.7	32.5	5.1
05/07/2024	28.5	34.6	1.5
06/07/2024	29.2	34	0.2
07/07/2024	29.6	34.8	Trace
08/07/2024	29.5	34.4	0.2
09/07/2024	28.9	34.3	Trace
10/07/2024	27	34.5	10.7
11/07/2024	28.5	32.2	6.5
12/07/2024	27.4	31.7	24.4
13/07/2024	27.7	33.8	8
14/07/2024	26.7	34.6	90
15/07/2024	27.9	33	13.6
16/07/2024	26	30.4	15.7
17/07/2024	26.7	32.7	13.7
18/07/2024	26.7	30.9	19.6
19/07/2024	27.1	30.8	40.5
20/07/2024	29	33.5	3.7
21/07/2024	28.6	32.1	4.7
22/07/2024	29	33.5	0.2
23/07/2024	28.8	33.3	0
24/07/2024	28.7	32.7	0
25/07/2024	29.5	33.1	Trace
26/07/2024	28.9	30.3	3.9
27/07/2024	27	30.2	34.7
28/07/2024	26.4	27.8	69.4
29/07/2024	26.6	29.6	6.7
30/07/2024	26.1	30.3	29.5
31/07/2024	26.2	30.2	48.2

NOTE1: The above weather information was obtained from manned weather station of Hong Kong Observatory.

NOTE2: race means rainfall less than 0.05 mm

<https://www.hko.gov.hk/en/cis/dailyExtract.htm?y=2024&m=7>

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
01/07/2024	0:00	0.4	157.5	02/07/2024	0:00	0.9	67.5	03/07/2024	0:00	0.4	67.5	04/07/2024	0:00	0.4	112.5
01/07/2024	1:00	0.4	67.5	02/07/2024	1:00	0.4	90	03/07/2024	1:00	0.4	112.5	04/07/2024	1:00	0.4	90
01/07/2024	2:00	0.4	22.5	02/07/2024	2:00	0.4	22.5	03/07/2024	2:00	0.9	22.5	04/07/2024	2:00	0.4	112.5
01/07/2024	3:00	0.4	225	02/07/2024	3:00	0.4	112.5	03/07/2024	3:00	0.9	90	04/07/2024	3:00	1.3	112.5
01/07/2024	4:00	0.9	315	02/07/2024	4:00	0.9	112.5	03/07/2024	4:00	0.9	292.5	04/07/2024	4:00	0.9	90
01/07/2024	5:00	0.9	337.5	02/07/2024	5:00	0.9	112.5	03/07/2024	5:00	0.4	292.5	04/07/2024	5:00	0.9	247.5
01/07/2024	6:00	0.4	67.5	02/07/2024	6:00	0.4	112.5	03/07/2024	6:00	0.4	292.5	04/07/2024	6:00	0.9	247.5
01/07/2024	7:00	0.4	112.5	02/07/2024	7:00	0.4	112.5	03/07/2024	7:00	0.9	22.5	04/07/2024	7:00	0.4	247.5
01/07/2024	8:00	0.4	135	02/07/2024	8:00	0.9	135	03/07/2024	8:00	0.4	22.5	04/07/2024	8:00	1.3	247.5
01/07/2024	9:00	0.9	45	02/07/2024	9:00	1.3	247.5	03/07/2024	9:00	1.3	45	04/07/2024	9:00	0.4	247.5
01/07/2024	10:00	0.4	22.5	02/07/2024	10:00	0.9	112.5	03/07/2024	10:00	0.9	22.5	04/07/2024	10:00	1.3	112.5
01/07/2024	11:00	0.9	135	02/07/2024	11:00	0.9	112.5	03/07/2024	11:00	0.4	22.5	04/07/2024	11:00	0.9	112.5
01/07/2024	12:00	0.9	157.5	02/07/2024	12:00	1.3	22.5	03/07/2024	12:00	1.3	22.5	04/07/2024	12:00	0.9	112.5
01/07/2024	13:00	0.9	157.5	02/07/2024	13:00	0.9	112.5	03/07/2024	13:00	1.3	180	04/07/2024	13:00	0.9	135
01/07/2024	14:00	0.9	112.5	02/07/2024	14:00	0.9	112.5	03/07/2024	14:00	0.9	90	04/07/2024	14:00	0.9	45
01/07/2024	15:00	0.9	90	02/07/2024	15:00	1.3	45	03/07/2024	15:00	0.4	22.5	04/07/2024	15:00	0.4	45
01/07/2024	16:00	0.9	90	02/07/2024	16:00	0.9	270	03/07/2024	16:00	0.9	90	04/07/2024	16:00	0.9	67.5
01/07/2024	17:00	1.3	67.5	02/07/2024	17:00	0.9	90	03/07/2024	17:00	1.8	112.5	04/07/2024	17:00	0.9	90
01/07/2024	18:00	1.3	67.5	02/07/2024	18:00	0.9	90	03/07/2024	18:00	1.3	67.5	04/07/2024	18:00	0.9	112.5
01/07/2024	19:00	1.3	135	02/07/2024	19:00	0.9	45	03/07/2024	19:00	0.9	45	04/07/2024	19:00	0.9	135
01/07/2024	20:00	0.9	112.5	02/07/2024	20:00	0.9	67.5	03/07/2024	20:00	1.3	45	04/07/2024	20:00	1.3	112.5
01/07/2024	21:00	1.8	90	02/07/2024	21:00	0.4	45	03/07/2024	21:00	1.3	67.5	04/07/2024	21:00	1.3	67.5
01/07/2024	22:00	1.3	112.5	02/07/2024	22:00	0.9	22.5	03/07/2024	22:00	1.3	67.5	04/07/2024	22:00	0.9	90
01/07/2024	23:00	0.9	90	02/07/2024	23:00	0.4	225	03/07/2024	23:00	1.8	45	04/07/2024	23:00	0.9	90

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
05/07/2024	0:00	1.3	112.5	06/07/2024	0:00	0.9	135	07/07/2024	0:00	0.4	247.5	08/07/2024	0:00	1.3	112.5
05/07/2024	1:00	1.3	67.5	06/07/2024	1:00	0.4	135	07/07/2024	1:00	2.2	247.5	08/07/2024	1:00	1.3	22.5
05/07/2024	2:00	1.8	112.5	06/07/2024	2:00	0.4	135	07/07/2024	2:00	1.3	90	08/07/2024	2:00	1.3	45
05/07/2024	3:00	0.9	90	06/07/2024	3:00	0.9	135	07/07/2024	3:00	1.8	90	08/07/2024	3:00	1.3	67.5
05/07/2024	4:00	1.3	90	06/07/2024	4:00	1.3	112.5	07/07/2024	4:00	1.3	135	08/07/2024	4:00	1.8	112.5
05/07/2024	5:00	1.3	90	06/07/2024	5:00	0.4	135	07/07/2024	5:00	1.3	135	08/07/2024	5:00	1.3	157.5
05/07/2024	6:00	1.8	112.5	06/07/2024	6:00	1.8	202.5	07/07/2024	6:00	0.9	135	08/07/2024	6:00	1.3	315
05/07/2024	7:00	1.8	112.5	06/07/2024	7:00	1.8	112.5	07/07/2024	7:00	1.3	337.5	08/07/2024	7:00	1.3	292.5
05/07/2024	8:00	0.9	112.5	06/07/2024	8:00	1.3	90	07/07/2024	8:00	1.3	22.5	08/07/2024	8:00	1.8	135
05/07/2024	9:00	1.8	45	06/07/2024	9:00	1.3	112.5	07/07/2024	9:00	1.3	315	08/07/2024	9:00	1.8	45
05/07/2024	10:00	1.8	22.5	06/07/2024	10:00	1.3	45	07/07/2024	10:00	0.9	112.5	08/07/2024	10:00	1.3	202.5
05/07/2024	11:00	0.9	292.5	06/07/2024	11:00	1.8	67.5	07/07/2024	11:00	0.9	315	08/07/2024	11:00	1.3	135
05/07/2024	12:00	0.9	67.5	06/07/2024	12:00	0.4	67.5	07/07/2024	12:00	0.4	292.5	08/07/2024	12:00	1.3	112.5
05/07/2024	13:00	1.3	292.5	06/07/2024	13:00	1.3	90	07/07/2024	13:00	0.4	135	08/07/2024	13:00	1.3	45
05/07/2024	14:00	1.8	112.5	06/07/2024	14:00	1.8	135	07/07/2024	14:00	0.4	135	08/07/2024	14:00	2.2	135
05/07/2024	15:00	1.8	135	06/07/2024	15:00	0.9	90	07/07/2024	15:00	0.4	112.5	08/07/2024	15:00	1.3	180
05/07/2024	16:00	0.9	135	06/07/2024	16:00	0.9	135	07/07/2024	16:00	1.3	45	08/07/2024	16:00	1.3	45
05/07/2024	17:00	0.9	135	06/07/2024	17:00	0.9	90	07/07/2024	17:00	1.3	45	08/07/2026	17:00	1.3	337.5
05/07/2024	18:00	0.9	315	06/07/2024	18:00	0.4	90	07/07/2024	18:00	1.3	337.5	08/07/2024	18:00	1.3	270
05/07/2024	19:00	0.9	112.5	06/07/2024	19:00	1.8	292.5	07/07/2024	19:00	1.3	90	08/07/2024	19:00	1.3	315
05/07/2024	20:00	2.2	292.5	06/07/2024	20:00	1.3	112.5	07/07/2024	20:00	0.9	112.5	08/07/2024	20:00	1.8	45
05/07/2024	21:00	0.9	45	06/07/2024	21:00	0.9	112.5	07/07/2024	21:00	0.9	22.5	08/07/2024	21:00	1.3	270
05/07/2024	22:00	1.3	45	06/07/2024	22:00	0.4	112.5	07/07/2024	22:00	0.9	270	08/07/2024	22:00	1.3	45
05/07/2024	23:00	1.3	45	06/07/2024	23:00	0.4	292.5	07/07/2024	23:00	0.9	270	08/07/2024	23:00	0.9	22.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
09/07/2024	0:00	1.3	112.5	10/07/2024	0:00	1.3	45	11/07/2024	0:00	0.9	337.5	12/07/2024	0:00	1.8	45
09/07/2024	1:00	1.8	67.5	10/07/2024	1:00	1.3	45	11/07/2024	1:00	0.9	90	12/07/2024	1:00	1.8	112.5
09/07/2024	2:00	1.3	292.5	10/07/2024	2:00	1.3	337.5	11/07/2024	2:00	0.9	337.5	12/07/2024	2:00	1.8	22.5
09/07/2024	3:00	1.3	112.5	10/07/2024	3:00	1.3	90	11/07/2024	3:00	0.9	22.5	12/07/2024	3:00	0.4	112.5
09/07/2024	4:00	1.8	135	10/07/2024	4:00	0.9	112.5	11/07/2024	4:00	0.4	270	12/07/2024	4:00	1.3	90
09/07/2024	5:00	1.8	112.5	10/07/2024	5:00	0.9	22.5	11/07/2024	5:00	0.4	270	12/07/2024	5:00	0.9	45
09/07/2024	6:00	1.3	135	10/07/2024	6:00	0.9	270	11/07/2024	6:00	0.4	225	12/07/2024	6:00	0.4	45
09/07/2024	7:00	1.3	45	10/07/2024	7:00	0.9	270	11/07/2024	7:00	0.9	270	12/07/2024	7:00	0.4	292.5
09/07/2024	8:00	1.8	337.5	10/07/2024	8:00	1.3	225	11/07/2024	8:00	0.9	202.5	12/07/2024	8:00	0.9	22.5
09/07/2024	9:00	0.9	247.5	10/07/2024	9:00	0.9	270	11/07/2024	9:00	0.4	135	12/07/2024	9:00	1.3	315
09/07/2024	10:00	0.9	112.5	10/07/2024	10:00	0.9	202.5	11/07/2024	10:00	0.4	135	12/07/2024	10:00	1.8	337.5
09/07/2024	11:00	0.4	112.5	10/07/2024	11:00	1.3	135	11/07/2024	11:00	0.4	135	12/07/2024	11:00	1.3	315
09/07/2024	12:00	0.4	112.5	10/07/2024	12:00	0.4	135	11/07/2024	12:00	0.4	135	12/07/2024	12:00	1.3	67.5
09/07/2024	13:00	0.9	135	10/07/2024	13:00	0.4	135	11/07/2024	13:00	0.4	112.5	12/07/2024	13:00	0.9	135
09/07/2024	14:00	0.4	112.5	10/07/2024	14:00	1.3	270	11/07/2024	14:00	0.9	135	12/07/2024	14:00	0.4	45
09/07/2024	15:00	0.9	90	10/07/2024	15:00	1.3	135	11/07/2024	15:00	1.3	67.5	12/07/2024	15:00	0.9	337.5
09/07/2024	16:00	0.4	135	10/07/2024	16:00	1.3	90	11/07/2024	16:00	0.4	45	12/07/2024	16:00	0.4	135
09/07/2024	17:00	0.9	135	10/07/2024	17:00	1.3	45	11/07/2024	17:00	1.3	112.5	12/07/2024	17:00	0.9	22.5
09/07/2024	18:00	1.3	112.5	10/07/2024	18:00	0.9	67.5	11/07/2024	18:00	0.9	45	12/07/2024	18:00	0.9	22.5
09/07/2024	19:00	0.4	135	10/07/2024	19:00	1.3	135	11/07/2024	19:00	1.3	90	12/07/2024	19:00	0.4	22.5
09/07/2024	20:00	1.8	202.5	10/07/2024	20:00	0.9	112.5	11/07/2024	20:00	0.9	45	12/07/2024	20:00	1.3	90
09/07/2024	21:00	1.8	112.5	10/07/2024	21:00	1.3	112.5	11/07/2024	21:00	0.4	67.5	12/07/2024	21:00	1.3	135
09/07/2024	22:00	1.3	90	10/07/2024	22:00	0.9	45	11/07/2024	22:00	0.9	135	12/07/2024	22:00	1.3	270
09/07/2024	23:00	1.3	112.5	10/07/2024	23:00	0.9	112.5	11/07/2024	23:00	0.4	90	12/07/2024	23:00	1.3	315

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
13/07/2024	0:00	1.3	45	14/07/2024	0:00	2.7	247.5	15/07/2024	0:00	0.4	247.5	16/07/2024	0:00	1.8	45
13/07/2024	1:00	1.8	67.5	14/07/2024	1:00	2.7	247.5	15/07/2024	1:00	1.3	247.5	16/07/2024	1:00	1.3	270
13/07/2024	2:00	2.7	112.5	14/07/2024	2:00	1.8	247.5	15/07/2024	2:00	0.9	180	16/07/2024	2:00	1.3	45
13/07/2024	3:00	0.9	202.5	14/07/2024	3:00	2.2	225	15/07/2024	3:00	2.7	180	16/07/2024	3:00	0.9	247.5
13/07/2024	4:00	0.9	45	14/07/2024	4:00	2.7	247.5	15/07/2024	4:00	1.3	292.5	16/07/2024	4:00	0.9	247.5
13/07/2024	5:00	0.9	90	14/07/2024	5:00	2.7	270	15/07/2024	5:00	1.8	67.5	16/07/2024	5:00	1.3	225
13/07/2024	6:00	0.9	135	14/07/2024	6:00	2.7	247.5	15/07/2024	6:00	1.3	90	16/07/2024	6:00	0.9	270
13/07/2024	7:00	0.9	90	14/07/2024	7:00	3.1	247.5	15/07/2024	7:00	1.3	157.5	16/07/2024	7:00	1.3	270
13/07/2024	8:00	0.4	90	14/07/2024	8:00	2.2	247.5	15/07/2024	8:00	0.9	112.5	16/07/2024	8:00	0.9	270
13/07/2024	9:00	1.8	292.5	14/07/2024	9:00	1.8	247.5	15/07/2024	9:00	0.9	67.5	16/07/2024	9:00	1.3	270
13/07/2024	10:00	1.3	112.5	14/07/2024	10:00	1.8	247.5	15/07/2024	10:00	0.4	135	16/07/2024	10:00	2.7	247.5
13/07/2024	11:00	0.9	112.5	14/07/2024	11:00	0.9	247.5	15/07/2024	11:00	0.4	157.5	16/07/2024	11:00	1.8	270
13/07/2024	12:00	0.4	112.5	14/07/2024	12:00	1.3	247.5	15/07/2025	12:00	0.4	157.5	16/07/2024	12:00	1.3	157.5
13/07/2024	13:00	1.3	112.5	14/07/2024	13:00	1.3	247.5	15/07/2024	13:00	0.4	112.5	16/07/2024	13:00	1.3	112.5
13/07/2024	14:00	0.4	112.5	14/07/2024	14:00	2.2	67.5	15/07/2024	14:00	0.4	112.5	16/07/2024	14:00	1.3	112.5
13/07/2024	15:00	0.9	135	14/07/2024	15:00	3.1	247.5	15/07/2024	15:00	0.4	112.5	16/07/2024	15:00	1.3	112.5
13/07/2024	16:00	1.8	112.5	14/07/2024	16:00	3.6	225	15/07/2024	16:00	0.9	180	16/07/2024	16:00	1.3	112.5
13/07/2024	17:00	0.9	112.5	14/07/2024	17:00	3.6	90	15/07/2024	17:00	0.9	112.5	16/07/2024	17:00	1.8	112.5
13/07/2024	18:00	1.8	90	14/07/2024	18:00	3.6	157.5	15/07/2024	18:00	0.4	90	16/07/2024	18:00	0.4	112.5
13/07/2024	19:00	1.3	135	14/07/2024	19:00	2.7	112.5	15/07/2024	19:00	0.4	135	16/07/2024	19:00	0.4	112.5
13/07/2024	20:00	1.3	135	14/07/2024	20:00	3.1	135	15/07/2024	20:00	0.4	90	16/07/2024	20:00	0.4	90
13/07/2024	21:00	0.9	135	14/07/2024	21:00	2.7	135	15/07/2024	21:00	0.4	90	16/07/2024	21:00	0.4	90
13/07/2024	22:00	1.3	337.5	14/07/2024	22:00	1.8	157.5	15/07/2024	22:00	0.4	112.5	16/07/2024	22:00	0.4	112.5
13/07/2024	23:00	1.3	90	14/07/2024	23:00	1.3	22.5	15/07/2024	23:00	0.9	67.5	16/07/2024	23:00	0.9	112.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
17/07/2024	0:00	0.9	112.5	18/07/2024	0:00	1.3	135	19/07/2024	0:00	2.2	90	20/07/2024	0:00	0.9	90
17/07/2024	1:00	0.9	112.5	18/07/2024	1:00	2.2	135	19/07/2024	1:00	1.8	135	20/07/2024	1:00	0.9	112.5
17/07/2024	2:00	1.3	202.5	18/07/2024	2:00	1.8	112.5	19/07/2024	2:00	1.3	135	20/07/2024	2:00	0.9	112.5
17/07/2024	3:00	0.9	112.5	18/07/2024	3:00	1.8	135	19/07/2024	3:00	1.8	90	20/07/2024	3:00	0.9	90
17/07/2024	4:00	0.4	112.5	18/07/2024	4:00	0.9	225	19/07/2024	4:00	0.9	112.5	20/07/2024	4:00	1.8	90
17/07/2024	5:00	0.4	45	18/07/2024	5:00	0.9	247.5	19/07/2024	5:00	1.8	337.5	20/07/2024	5:00	1.3	90
17/07/2024	6:00	0.9	112.5	18/07/2024	6:00	0.4	247.5	19/07/2024	6:00	1.3	112.5	20/07/2024	6:00	0.9	157.5
17/07/2024	7:00	0.9	157.5	18/07/2024	7:00	0.4	157.5	19/07/2024	7:00	1.3	90	20/07/2024	7:00	1.3	112.5
17/07/2024	8:00	0.9	292.5	18/07/2024	8:00	0.9	112.5	19/07/2024	8:00	1.3	90	20/07/2024	8:00	0.9	112.5
17/07/2024	9:00	0.4	112.5	18/07/2024	9:00	0.9	45	19/07/2024	9:00	1.3	112.5	20/07/2024	9:00	1.3	112.5
17/07/2024	10:00	0.4	247.5	18/07/2024	10:00	0.4	270	19/07/2024	10:00	0.4	112.5	20/07/2024	10:00	1.8	202.5
17/07/2024	11:00	0.9	315	18/07/2024	11:00	0.4	247.5	19/07/2024	11:00	0.9	112.5	20/07/2024	11:00	1.3	135
17/07/2024	12:00	0.4	315	18/07/2024	12:00	0.4	247.5	19/07/2024	12:00	2.2	202.5	20/07/2024	12:00	1.3	112.5
17/07/2024	13:00	0.4	135	18/07/2024	13:00	0.4	292.5	19/07/2024	13:00	1.8	135	20/07/2024	13:00	0.9	202.5
17/07/2024	14:00	0.9	112.5	18/07/2024	14:00	0.9	225	19/07/2024	14:00	1.8	112.5	20/07/2024	14:00	0.9	90
17/07/2024	15:00	0.9	45	18/07/2024	15:00	0.9	247.5	19/07/2024	15:00	2.2	112.5	20/07/2024	15:00	0.4	67.5
17/07/2024	16:00	1.3	112.5	18/07/2024	16:00	0.4	247.5	19/07/2024	16:00	1.8	112.5	20/07/2024	16:00	0.4	157.5
17/07/2024	17:00	0.9	112.5	18/07/2024	17:00	0.4	157.5	19/07/2024	17:00	1.3	67.5	20/07/2024	17:00	0.9	67.5
17/07/2024	18:00	0.4	90	18/07/2024	18:00	0.9	112.5	19/07/2024	18:00	1.8	67.5	20/07/2024	18:00	0.4	67.5
17/07/2024	19:00	0.9	90	18/07/2024	19:00	0.9	157.5	19/07/2024	19:00	0.9	45	20/07/2024	19:00	1.3	112.5
17/07/2024	20:00	1.3	90	18/07/2024	20:00	0.4	157.5	19/07/2024	20:00	1.8	112.5	20/07/2024	20:00	0.4	292.5
17/07/2024	21:00	1.8	90	18/07/2024	21:00	0.9	247.5	19/07/2024	21:00	1.3	135	20/07/2024	21:00	0.4	135
17/07/2024	22:00	1.3	135	18/07/2024	22:00	0.4	112.5	19/07/2024	22:00	1.3	135	20/07/2024	22:00	0.9	135
17/07/2024	23:00	0.9	67.5	18/07/2024	23:00	0.9	112.5	19/07/2024	23:00	1.3	112.5	20/07/2024	23:00	0.9	90

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
21/07/2024	0:00	0.9	45	22/07/2024	0:00	0.4	90	23/07/2024	0:00	0.9	225	24/07/2024	0:00	0.4	90
21/07/2024	1:00	0.4	67.5	22/07/2024	1:00	0.4	22.5	23/07/2024	1:00	0.4	202.5	24/07/2024	1:00	0.4	22.5
21/07/2024	2:00	0.4	157.5	22/07/2024	2:00	1.3	90	23/07/2024	2:00	0	202.5	24/07/2024	2:00	1.3	90
21/07/2024	3:00	0.4	180	22/07/2024	3:00	0.9	112.5	23/07/2024	3:00	0.4	225	24/07/2024	3:00	0.9	112.5
21/07/2024	4:00	0.9	45	22/07/2024	4:00	1.3	45	23/07/2024	4:00	0.4	202.5	24/07/2024	4:00	0.9	112.5
21/07/2024	5:00	0.9	112.5	22/07/2024	5:00	1.3	135	23/07/2024	5:00	0	202.5	24/07/2024	5:00	0.9	135
21/07/2024	6:00	0.9	112.5	22/07/2024	6:00	0.9	157.5	23/07/2024	6:00	0.4	112.5	24/07/2024	6:00	0.9	90
21/07/2024	7:00	0.4	112.5	22/07/2024	7:00	0.9	112.5	23/07/2024	7:00	0	112.5	24/07/2024	7:00	0.9	112.5
21/07/2024	8:00	0.4	135	22/07/2024	8:00	0.4	90	23/07/2024	8:00	0.4	112.5	24/07/2024	8:00	1.8	112.5
21/07/2024	9:00	1.3	112.5	22/07/2024	9:00	0.9	67.5	23/07/2024	9:00	0.4	112.5	24/07/2024	9:00	1.3	112.5
21/07/2024	10:00	0.4	90	22/07/2024	10:00	0.9	112.5	23/07/2024	10:00	0.4	112.5	24/07/2024	10:00	0.9	90
21/07/2024	11:00	0.9	90	22/07/2024	11:00	0.9	45	23/07/2024	11:00	1.3	112.5	24/07/2024	11:00	1.8	90
21/07/2024	12:00	0.9	112.5	22/07/2024	12:00	0.4	135	23/07/2024	12:00	0.4	90	24/07/2024	12:00	1.3	90
21/07/2024	13:00	0.4	90	22/07/2024	13:00	0.9	67.5	23/07/2024	13:00	0.4	22.5	24/07/2024	13:00	1.8	67.5
21/07/2024	14:00	1.3	112.5	22/07/2024	14:00	0.4	135	23/07/2024	14:00	1.3	90	24/07/2024	14:00	0.9	112.5
21/07/2024	15:00	0.4	135	22/07/2024	15:00	0.4	67.5	23/07/2024	15:00	0.9	112.5	24/07/2024	15:00	1.8	22.5
21/07/2024	16:00	0.4	67.5	22/07/2024	16:00	0.9	67.5	23/07/2024	16:00	0.9	112.5	24/07/2024	16:00	0.9	270
21/07/2024	17:00	0.9	67.5	22/07/2024	17:00	0.9	90	23/07/2024	17:00	0.9	135	24/07/2024	17:00	1.3	0
21/07/2024	18:00	0.9	90	22/07/2024	18:00	0.9	90	23/07/2024	18:00	0.9	90	24/07/2024	18:00	1.3	270
21/07/2024	19:00	0.9	90	22/07/2024	19:00	0.9	90	23/07/2024	19:00	0.9	112.5	24/07/2024	19:00	0.4	337.5
21/07/2024	20:00	0.9	90	22/07/2024	20:00	1.3	67.5	23/07/2024	20:00	1.8	112.5	24/07/2024	20:00	1.3	270
21/07/2024	21:00	1.3	67.5	22/07/2024	21:00	0.9	67.5	23/07/2024	21:00	1.3	112.5	24/07/2024	21:00	0.9	247.5
21/07/2024	22:00	0.9	67.5	22/07/2024	22:00	1.3	67.5	23/07/2024	22:00	0.9	90	24/07/2024	22:00	0.4	225
21/07/2024	23:00	1.3	90	22/07/2024	23:00	0.9	67.5	23/07/2024	23:00	1.8	90	24/07/2024	23:00	0.4	180

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
25/07/2024	0:00	2.2	112.5	26/07/2024	0:00	0.4	45	27/07/2024	0:00	1.3	90	28/07/2024	0:00	1.3	90
25/07/2024	1:00	2.2	90	26/07/2024	1:00	0.9	67.5	27/07/2024	1:00	1.8	67.5	28/07/2024	1:00	0.9	270
25/07/2024	2:00	2.7	112.5	26/07/2024	2:00	0.9	135	27/07/2024	2:00	0.9	112.5	28/07/2024	2:00	0.4	225
25/07/2024	3:00	1.8	112.5	26/07/2024	3:00	0.9	45	27/07/2024	3:00	0.4	112.5	28/07/2024	3:00	0.9	225
25/07/2024	4:00	2.2	90	26/07/2024	4:00	0.9	247.5	27/07/2024	4:00	0.4	90	28/07/2024	4:00	1.3	292.5
25/07/2024	5:00	1.3	90	26/07/2024	5:00	0.4	225	27/07/2024	5:00	0.9	112.5	28/07/2024	5:00	0.9	247.5
25/07/2024	6:00	1.3	112.5	26/07/2024	6:00	0.9	67.5	27/07/2024	6:00	0.9	90	28/07/2024	6:00	1.8	270
25/07/2024	7:00	1.3	112.5	26/07/2024	7:00	0.4	270	27/07/2024	7:00	1.3	90	28/07/2024	7:00	2.2	270
25/07/2024	8:00	2.2	112.5	26/07/2024	8:00	0.4	247.5	27/07/2024	8:00	1.3	112.5	28/07/2024	8:00	1.3	135
25/07/2024	9:00	2.2	90	26/07/2024	9:00	0.4	180	27/07/2024	9:00	0.9	90	28/07/2024	9:00	0.9	315
25/07/2024	10:00	2.7	112.5	26/07/2024	10:00	0.4	247.5	27/07/2024	10:00	0.9	90	28/07/2024	10:00	0.4	315
25/07/2024	11:00	1.8	112.5	26/07/2024	11:00	0.4	270	27/07/2024	11:00	1.3	112.5	28/07/2024	11:00	0.9	45
25/07/2024	12:00	2.2	90	26/07/2024	12:00	0.4	135	27/07/2024	12:00	1.3	112.5	28/07/2024	12:00	0.9	247.5
25/07/2024	13:00	1.3	90	26/07/2024	13:00	0.4	157.5	27/07/2024	13:00	0.9	135	28/07/2024	13:00	1.8	270
25/07/2024	14:00	1.3	112.5	26/07/2024	14:00	0.4	157.5	27/07/2024	14:00	0.9	112.5	28/07/2024	14:00	1.3	270
25/07/2024	15:00	1.3	112.5	26/07/2024	15:00	0.4	202.5	27/07/2024	15:00	0.4	112.5	28/07/2024	15:00	1.8	270
25/07/2024	16:00	0.9	135	26/07/2024	16:00	1.3	225	27/07/2024	16:00	0.9	112.5	28/07/2024	16:00	1.3	247.5
25/07/2024	17:00	1.3	90	26/07/2024	17:00	1.3	247.5	27/07/2024	17:00	0.4	112.5	28/07/2024	17:00	1.3	135
25/07/2024	18:00	0.9	112.5	26/07/2024	18:00	0.9	135	27/07/2024	18:00	0.4	112.5	28/07/2024	18:00	1.3	135
25/07/2024	19:00	0.9	112.5	26/07/2024	19:00	0.9	112.5	27/07/2024	19:00	0.9	135	28/07/2024	19:00	1.8	135
25/07/2024	20:00	1.8	112.5	26/07/2024	20:00	1.3	22.5	27/07/2024	20:00	0.9	112.5	28/07/2024	20:00	1.3	202.5
25/07/2024	21:00	0.4	90	26/07/2024	21:00	1.3	135	27/07/2024	21:00	0.9	112.5	28/07/2024	21:00	0.9	270
25/07/2024	22:00	1.3	45	26/07/2024	22:00	2.2	90	27/07/2024	22:00	1.3	90	28/07/2024	22:00	1.3	247.5
25/07/2024	23:00	0.9	112.5	26/07/2024	23:00	1.8	112.5	27/07/2024	23:00	0.9	112.5	28/07/2024	23:00	1.3	225

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Hong Kong Children's Hospital

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
29/07/2024	0:00	0.9	247.5	30/07/2024	0:00	0.9	247.5	31/07/2024	0:00	2.2	247.5				
29/07/2024	1:00	1.3	247.5	30/07/2024	1:00	0.9	247.5	31/07/2024	1:00	2.2	270				
29/07/2024	2:00	0.9	270	30/07/2024	2:00	1.3	247.5	31/07/2024	2:00	2.7	247.5				
29/07/2024	3:00	1.3	247.5	30/07/2024	3:00	0.9	270	31/07/2024	3:00	1.8	225				
29/07/2024	4:00	0.9	270	30/07/2024	4:00	1.3	247.5	31/07/2024	4:00	2.2	247.5				
29/07/2024	5:00	0.4	247.5	30/07/2024	5:00	0.9	112.5	31/07/2024	5:00	2.7	247.5				
29/07/2024	6:00	0.9	225	30/07/2024	6:00	0.9	67.5	31/07/2024	6:00	2.7	247.5				
29/07/2024	7:00	1.3	247.5	30/07/2024	7:00	0.9	90	31/07/2024	7:00	2.2	225				
29/07/2024	8:00	0.9	247.5	30/07/2024	8:00	0.9	157.5	31/07/2024	8:00	2.2	270				
29/07/2024	9:00	1.8	90	30/07/2024	9:00	1.3	112.5	31/07/2024	9:00	2.2	45				
29/07/2024	10:00	0.4	67.5	30/07/2024	10:00	0.9	112.5	31/07/2024	10:00	2.7	112.5				
29/07/2024	11:00	0.9	67.5	30/07/2024	11:00	1.3	112.5	31/07/2024	11:00	1.8	135				
29/07/2024	12:00	0.4	67.5	30/07/2024	12:00	1.8	202.5	31/07/2024	12:00	2.2	135				
29/07/2024	13:00	0.9	45	30/07/2024	13:00	1.3	135	31/07/2024	13:00	1.3	112.5				
29/07/2024	14:00	0.4	67.5	30/07/2024	14:00	1.3	112.5	31/07/2024	14:00	1.8	112.5				
29/07/2024	15:00	1.3	225	30/07/2024	15:00	0.9	202.5	31/07/2024	15:00	1.3	45				
29/07/2024	16:00	1.8	247.5	30/07/2024	16:00	0.9	90	31/07/2024	16:00	1.8	112.5				
29/07/2024	17:00	1.3	247.5	30/07/2024	17:00	0.4	67.5	31/07/2024	17:00	1.8	157.5				
29/07/2024	18:00	1.3	90	30/07/2024	18:00	0.4	157.5	31/07/2024	18:00	1.8	292.5				
29/07/2024	19:00	1.3	45	30/07/2024	19:00	0.9	67.5	31/07/2024	19:00	1.3	112.5				
29/07/2024	20:00	1.3	247.5	30/07/2024	20:00	0.4	67.5	31/07/2024	20:00	1.3	247.5				
29/07/2024	21:00	1.8	112.5	30/07/2024	21:00	1.3	112.5	31/07/2024	21:00	1.3	315				
29/07/2024	22:00	1.8	112.5	30/07/2024	22:00	0.4	112.5	31/07/2024	22:00	1.3	315				
29/07/2024	23:00	0.4	135	30/07/2024	23:00	0.4	112.5	31/07/2024	23:00	0.4	135				

Appendix H – 24-hr TSP monitoring results and graphical presentation

Location: AM3 – Sky Tower

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m³/min)	Total vol. (m³)	Conc. (µg/m³)
				Initial	Final		Initial	Final		Initial	Final			
05/07/2024	Sunny	33.1	1008.8	15.1076	15.2187	0.1111	2024/7/5 9:31	2024/7/6 9:31	1440.0	46	46	1.26	1810	61
11/07/2024	Cloudy	33.8	1006.8	15.1351	15.2824	0.1473	2024/7/11 13:26	2024/7/12 13:26	1440.0	48	48	1.31	1885	78
17/07/2024	Cloudy	32.6	1008.9	15.1922	15.2907	0.0985	2024/7/17 9:33	2024/7/18 9:33	1440.0	46	46	1.26	1811	54
23/07/2024	Sunny	35.2	1001.6	18.2391	18.3268	0.0877	2024/7/23 9:34	2024/7/24 9:34	1440.0	46	46	1.25	1797	49
29/07/2024	Cloudy	28.9	1006.1	17.8232	17.8809	0.0577	2024/7/29 13:25	2024/7/30 13:25	1440.0	46	46	1.26	1820	32
												Maximum		78
												Minimum		32
												Average		55
												Action Level		182
												Limit Level		260


Location: AM4(A) - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A) ET will resume the impact monitoring once the alternative monitoring location for AM4(A) is confirmed.


Location: AM7 – Hong Kong Children’s Hospital

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m³/min)	Total vol. (m³)	Conc. (µg/m³)
				Initial	Final		Initial	Final		Initial	Final			
05/07/2024	Sunny	33.1	1008.8	15.1347	15.1983	0.0636	2024/7/5 9:33	2024/7/6 9:33	1440.0	50	50	1.40	2010	32
11/07/2024	Cloudy	33.8	1006.8	18.0694	18.1487	0.0793	2024/7/11 13:34	2024/7/12 13:34	1440.0	50	50	1.39	2006	40
17/07/2024	Cloudy	32.6	1008.9	18.1769	18.3032	0.1263	2024/7/17 9:37	2024/7/18 9:37	1440.0	51	51	1.43	2052	62
23/07/2024	Sunny	35.2	1001.6	18.0285	18.1328	0.1043	2024/7/23 13:28	2024/7/24 13:28	1440.0	51	51	1.41	2036	51
29/07/2024	Cloudy	28.9	1006.1	15.0789	15.1277	0.0488	2024/7/29 9:50	2024/7/30 9:50	1440.0	51	51	1.43	2062	24
												Maximum		62
												Minimum		24
												Average		42
												Action Level		181
												Limit Level		260

24-hour average TSP

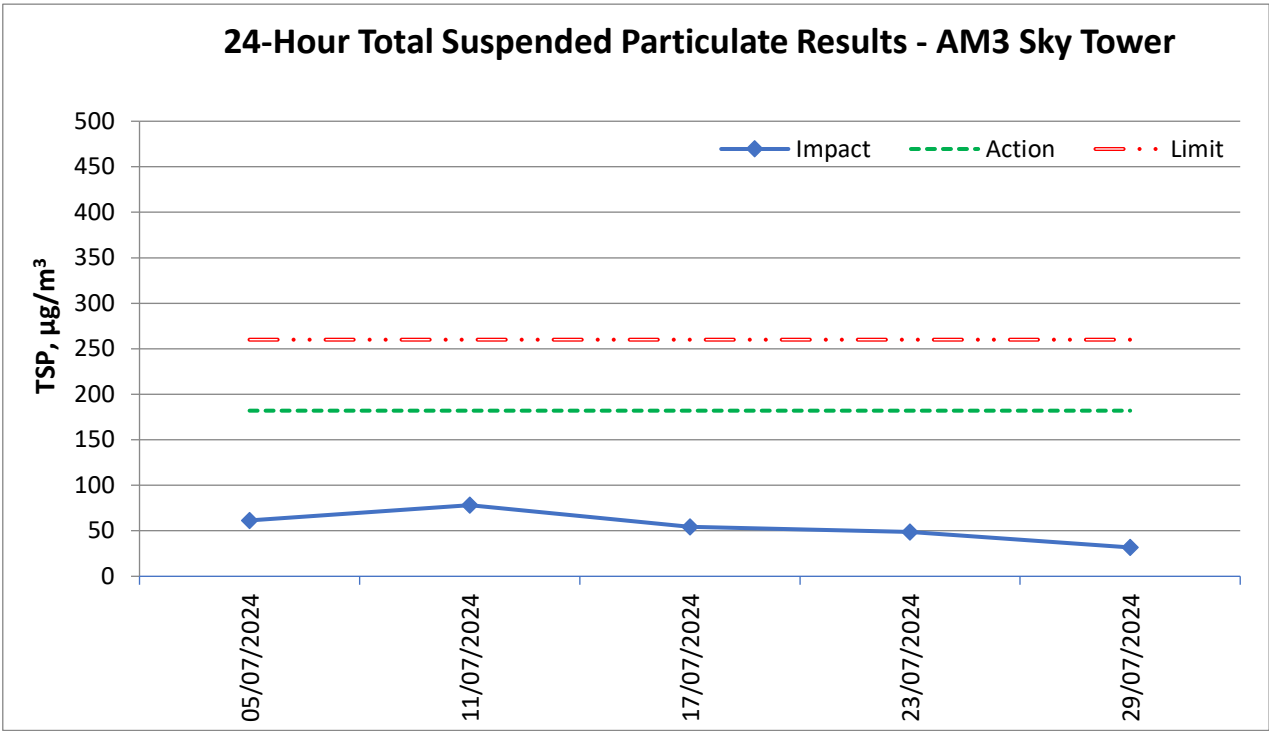

Note: Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. No 24-TSP monitoring was conducted at AM4(A). ET will resume the impact monitoring once the alternative monitoring location for AM4(A) is confirmed.

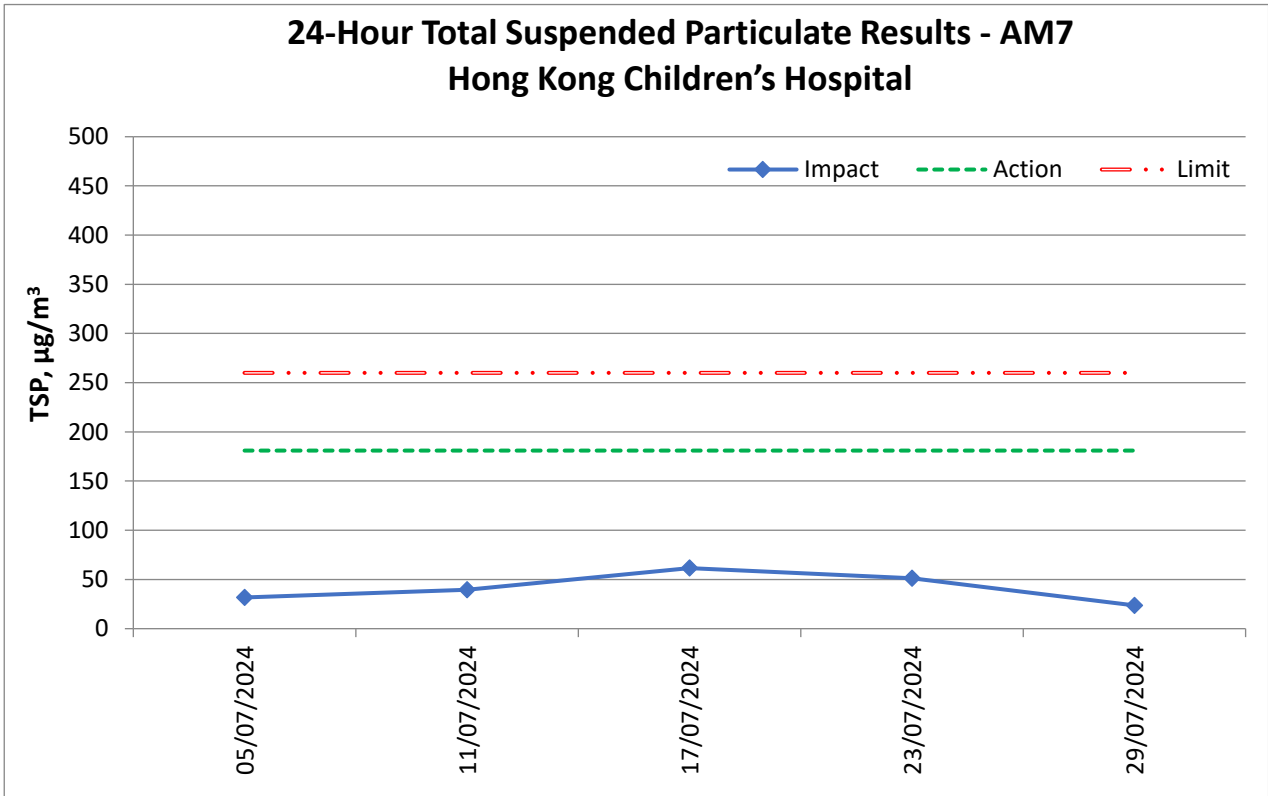

Appendix I – 1-hr TSP monitoring results and graphical presentation

Location:
**AM3 -
 Sky Tower**

Date	Measurement Period			1-hr TSP concentration, g/m ³	Weather
05/07/2024	9:00	-	10:00	72	Sunny
	10:00	-	11:00	74	
	11:00	-	12:00	77	
11/07/2024	13:00	-	14:00	73	Cloudy
	14:00	-	15:00	76	
	15:00	-	16:00	75	
17/07/2024	9:00	-	10:00	46	Cloudy
	10:00	-	11:00	44	
	11:00	-	12:00	41	
23/07/2024	9:00	-	10:00	35	Sunny
	10:00	-	11:00	40	
	11:00	-	12:00	42	
29/07/2024	13:00	-	14:00	31	Cloudy
	14:00	-	15:00	36	
	15:00	-	16:00	35	
Maximum				77	
Minimum				31	
Average				53	
Action Level				297	
Limit Level				500	

Location:
**AM4(A) -
The Hong Kong
Society for the
Blind's Factory
cum Sheltered
Workshop**



Date	Measurement Period			1-hr TSP concentration, $\mu\text{g}/\text{m}^3$	Weather
05/07/2024	13:00	-	14:00	84	Sunny
	14:00	-	15:00	88	
	15:00	-	16:00	88	
11/07/2024	9:00	-	10:00	81	Cloudy
	10:00	-	11:00	81	
	11:00	-	12:00	83	
17/07/2024	13:00	-	14:00	53	Cloudy
	14:00	-	15:00	51	
	15:00	-	16:00	50	
23/07/2024	9:00	-	10:00	46	Sunny
	10:00	-	11:00	44	
	11:00	-	12:00	44	
29/07/2024	13:00	-	14:00	35	Cloudy
	14:00	-	15:00	37	
	15:00	-	16:00	34	
Maximum				88	
Minimum				34	
Average				60	
Action Level				326	
Limit Level				500	

NOTE: Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 1-hr TSP monitoring at AM4(A) were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for AM4(A) is confirmed.

Location:
AM7 -
Hong Kong
Children's
Hospital


Date	Measurement Period			1-hr TSP concentration, $\mu\text{g}/\text{m}^3$	Weather
05/07/2024	9:00	-	10:00	57	Sunny
	10:00	-	11:00	59	
	11:00	-	12:00	60	
11/07/2024	13:00	-	14:00	48	Cloudy
	14:00	-	15:00	49	
	15:00	-	16:00	52	
17/07/2024	9:00	-	10:00	36	Cloudy
	10:00	-	11:00	34	
	11:00	-	12:00	33	
23/07/2024	13:00	-	14:00	43	Sunny
	14:00	-	15:00	47	
	15:00	-	16:00	51	
29/07/2024	9:00	-	10:00	33	Cloudy
	10:00	-	11:00	38	
	11:00	-	12:00	37	
Maximum				60	
Minimum				33	
Average				45	
Action Level				315	
Limit Level				500	

1-hour average TSP

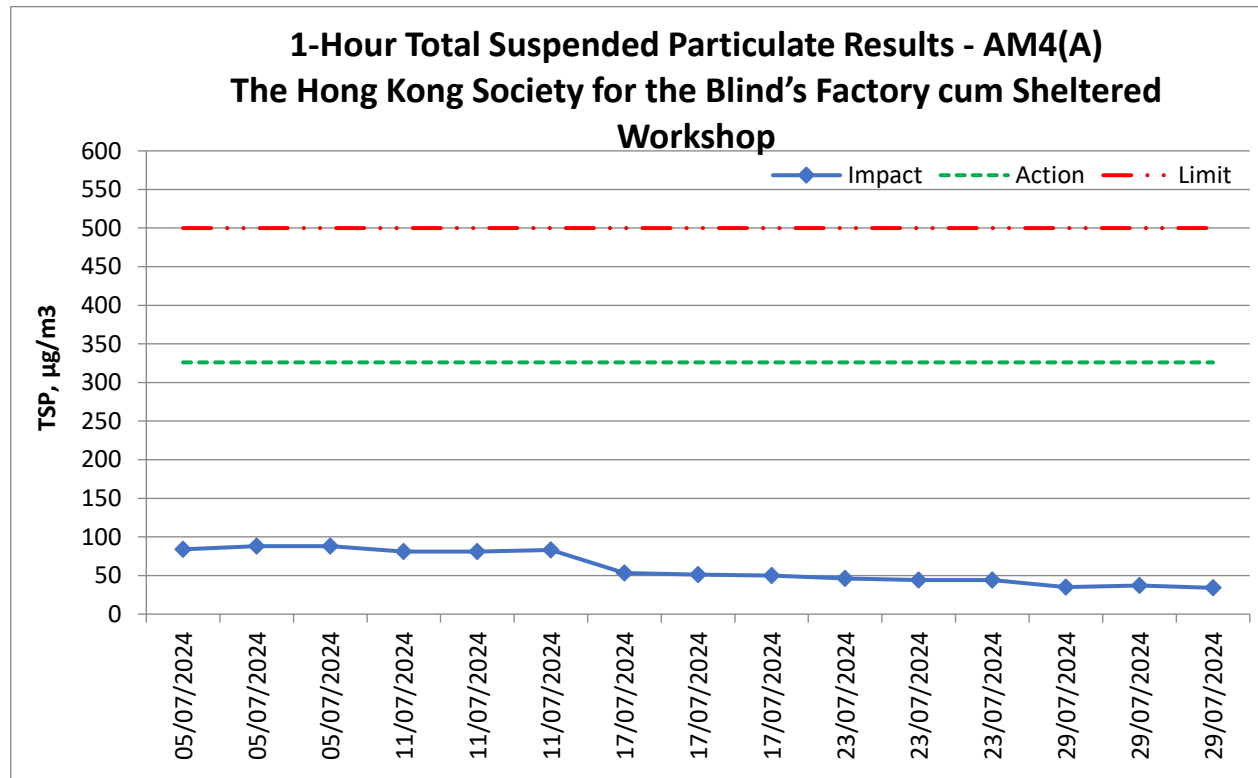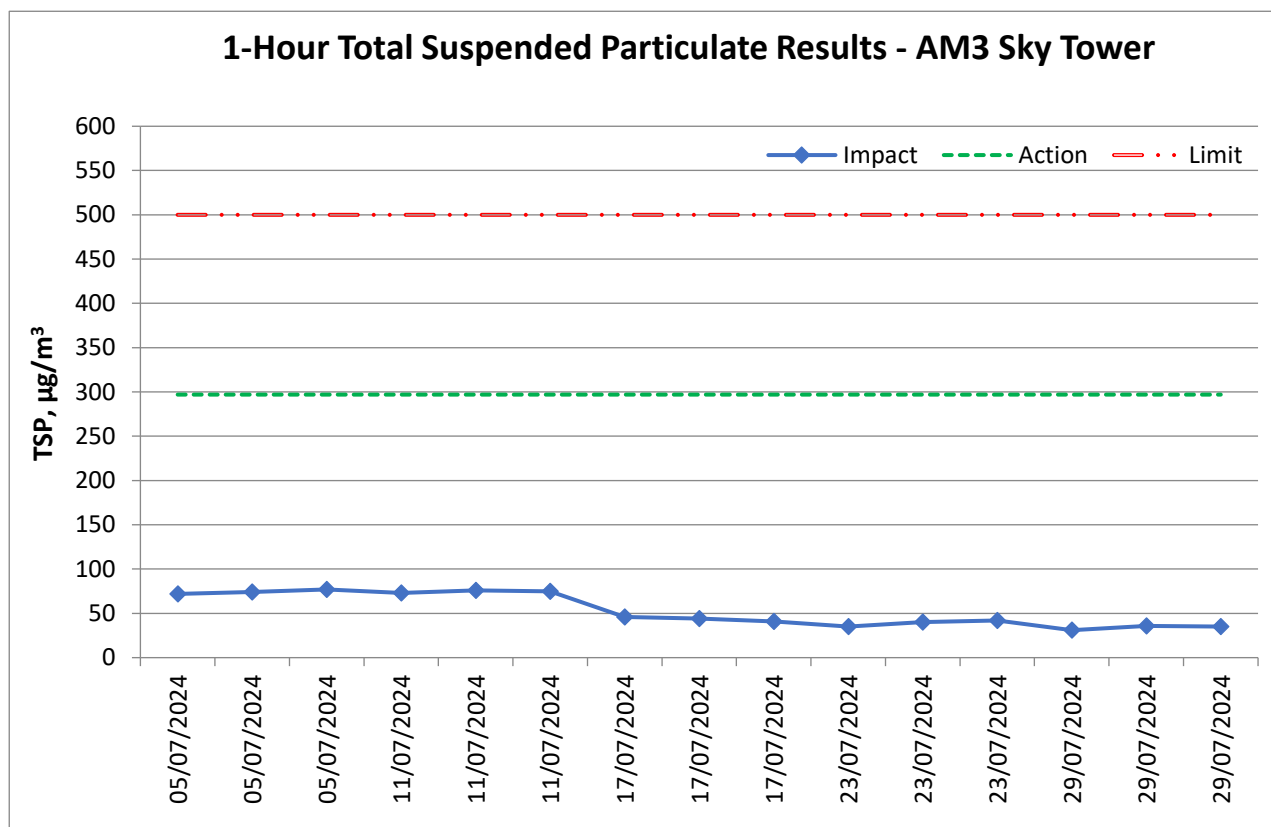

NOTE: Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (AM4(A)), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 1-hr TSP monitoring at AM4(A) were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for AM4(A) is confirmed.

1-Hour Total Suspended Particulate Results - AM7 Hong Kong Children's Hospital

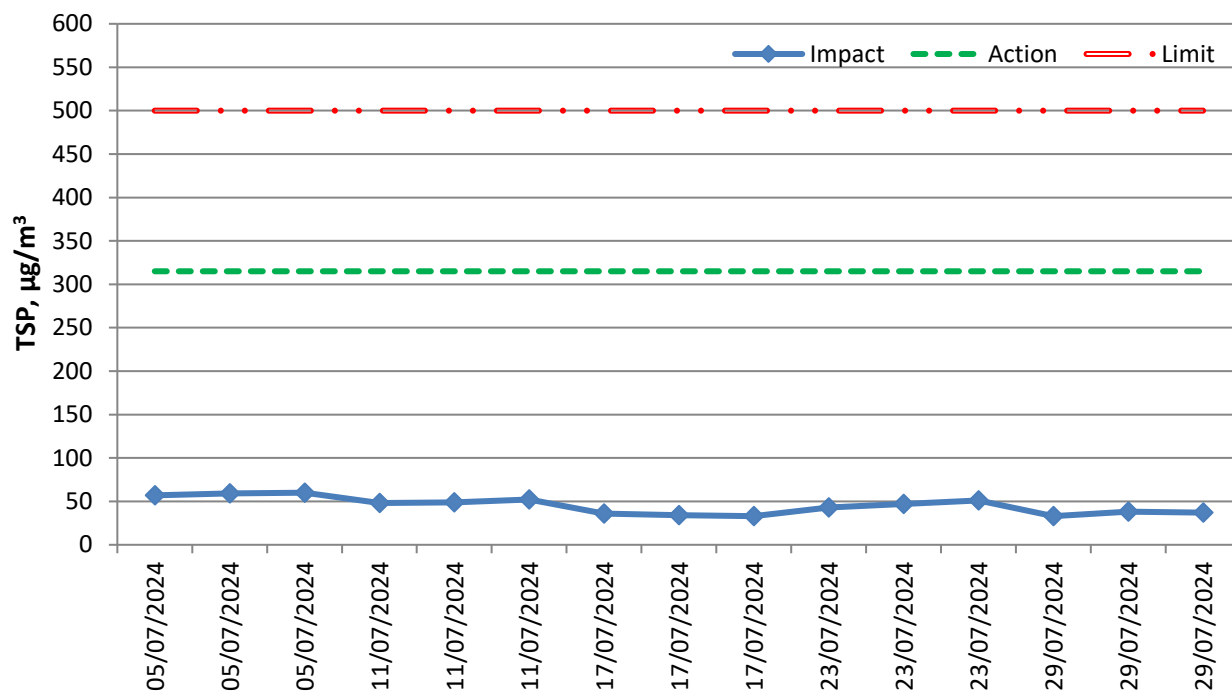

Appendix J – Event and Action Plan for air quality

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded by one sampling	1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC and Supervisor /ER; 3. Repeat measurement to confirm finding.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action Level being exceeded by two or more consecutive sampling	1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC and Supervisor /ER; 3. Increase monitoring frequency to daily; 4. Discuss with IEC and Contractor on remedial actions required; 5. Assess the effectiveness of Contractor's remedial actions; 6. If exceedance continues, arrange meeting with IEC and Supervisor /ER; 7. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the Supervisor /ER on the effectiveness of the proposed remedial measures.	1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues.	1. Discuss with ET and IEC on proper remedial actions; 2. Submit proposals for remedial actions to Supervisor /ER and IEC within three working day of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Limit Level being exceeded by one sampling	1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC, Supervisor /ER, and EPD; 3. Repeat measurement to confirm finding; 4. Assess effectiveness of	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss possible remedial measures with ET and Contractor; 4. Advise the Supervisor /ER	1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on proper remedial actions; 3. Submit proposal for remedial actions to Supervisor /ER and IEC

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results.	on the effectiveness of the proposed remedial measures.	4. implemented; Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues.	within three working days of notification; 4. Implement the agreed proposals.
Limit Level being exceeded by two or more consecutive sampling	1. Notify IEC, Supervisor /ER, Contractor and EPD; 2. Repeat measurement to confirm findings; 3. Carry out analysis of Contractor's working procedures to identify source and investigate the causes of exceedance; 4. Increase monitoring frequency to daily; 5. Arrange meeting with IEC, Supervisor /ER and Contractor to discuss the remedial action to be taken; 6. Assess effectiveness of Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results; 7. If exceedance stop, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with Supervisor /ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly.	1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on proper remedial actions; 3. Submit proposal for remedial actions to Supervisor /ER and IEC within three working days of notification; 4. Implement the agreed proposals; 5. Submit further remedial actions if problem still not under control; 6. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated.

Appendix K – Calibration certificates, catalogue of noise monitoring equipment

Catalogue of Sound Level Meter

Specifications

NL-52		NL-42	
Applicable standards		IEC 61672-1: 2002 Class 1 ANSI S1.4-1983 Type 1 ANSI S1.4A-1985 Type 1 ANSI S1.43-1997 Type 1 JIS C 1509-1: 2005 Class 1 CE Marking: EMC Directive 2004/108/EC, Low Voltage Directive 2006/95/EC, WEEE Directives, Chinese RoHS (export model for China only)	
Measurement functions		Simultaneous measurement of the following items, with selected time weighting and frequency weighting Processing (main ch) Instantaneous sound pressure level: L_p Equivalent continuous sound pressure level: L_{eq} Sound exposure level: L_s Maximum sound pressure level: L_{max} Minimum sound pressure level: L_{min} Percentile sound levels: L_N (0.1 to 99.9 %, 0.1-increment steps, max. 5 values) Processing (sub ch) Instantaneous sound pressure level: L_p Additional processing In addition to main processing items, one of the following can be selected for simultaneous processing: C-weighted equivalent continuous sound level: L_{Ceq} C-weighted peak sound level: L_{Cpeak} Z-weighted peak sound level: L_{Zpeak} 1-time-weighted equivalent continuous sound level: $L_{A,1eq}^{*2}$ Maximum 1-time-weighted equivalent continuous sound level: $L_{A,1max}^{*2}$ The power average of the maximum level of each 5 second interval: $L_{A,5}$ The frequency weighting for the additional processing synchronizes with the frequency weighting of the sub-channel, so when the sub-channel has A-weighting, $L_{A,5}$ can be selected. When C-weighting (Z-weighting) is selected, the additional processing L_{Ceq} and L_{Cpeak} (L_{Zpeak}) are selectable.	
Measuring time		10 s, 1, 5, 10, 15, 30 m, 1, 8, 24 h, and manual (maximum 24 h)	
Microphone	Type	UC-59	
	Sensitivity level	-27 dB	
Measurement range		A-weighting: 25 dB to 138 dB C-weighting: 33 dB to 138 dB Z-weighting: 38 dB to 138 dB C-weighting peak sound level: 55 dB to 141 dB Z-weighting peak sound level: 60 dB to 141 dB	
Inherent noise	A-weighting	17 dB or less	
	C-weighting	25 dB or less	
	Z-weighting	30 dB or less	
Frequency range		20 Hz to 20 kHz	
Frequency weighting		A, C, and Z	
Time weighting		F (Fast) and S (Slow)	
Level range		Single range (Linearity range: 113 dB)	
Bar graph display range max		Max. 110 dB (20 to 130 dB)	
Switching of bar graph display		Set the upper/lower limit in 10 dB increments.	
RMS detection circuit		Digital processing method	
Sampling cycle		20.8 μ s (L_p , L_{eq} , L_s , L_{max} , L_{min} , L_{peak} : sampling frequency: 48 kHz) 100 ms (L_N)	
Calibration		Measurement Law: electrical calibration performed according to IEC and JIS standards, using internally generated signals: acoustic calibration performed with the NC-74.	
Correction functions		Windscreen correction: Compliant with IEC 61672-1 and JIS C 1509-1 standards when the windscreen is installed. Diffuse sound field correction: Correction of frequency characteristics in order to comply with standards (ANSI S1.4) in diffuse sound field.	
Delay time		The meter can be set to start measuring a specified time (OFF, 1, 3, 5 or 10 s) after the start button has been pressed or when a user-set trigger is exceeded.	
Back erase function		When the PAUSE key is pressed to pause measurement, the preceding (user selectable) 0, 1, 3 or 5 s data are excluded from processing.	
Display		Backlit semitransparent color TFT LCD display WQVGA (400 x 240 dots) * LCD with touch panel (Capacitive Touch Panel) Numerical display update frequency: 1 s Bar graph update frequency: 100 ms	
Store	Manual	Data for measurement results are stored manually in single address increments.	
	Auto+2	Internal memory: max. 1000 sets SD Card: depends on the capacity of the SD Card*1 Instantaneous values (L_p mode) and processed values (L_{eq} mode) are stored continuously and automatically at preset intervals.	
Lp sampling cycle		100 ms, 200 ms, 1 s, L_{eq} 1 s	
Leq sampling cycle		10 s, 1, 5, 10, 15, 30 ms, 1, 8, 24 h	
Measurement Time		Max. 1000 h (depends on the capacity of the SD Card)*1	

Data recall	Allows viewing of stored data
Setup memory	Up to five setup configurations can be saved in internal memory, for later recall Start up via file settings previously stored on SD card possible
Waveform recording*3	
File format	Uncompressed waveform WAVE file
Sampling frequency	Select 48 kHz, 24 kHz or 12 kHz
Data length	Select 24 bit or 16 bit
Outputs	
DC output	Output DC signals using a frequency weighting characteristic selected by processing
Output voltage	2.5 V, 25 mV / dB at bar graph display full scale
AC output	Output AC signals using a frequency weighting characteristic selected by processing or by A, C, Z-weighting.
Output voltage	1 V (rms values) at bar graph display full scale
Comparator output*2	Turns on when the open-collector output exceeds the set value (max. applied voltage 24 V, max. current 60 mA, allowable dissipation 300 mW).
USB	Allows USB to be connected to a computer and recognized as a removable disk Allows USB to be controlled via communication commands
RS-232C communication	Allows for RS-232C communication via use of a dedicated cable
Data continuous output*2	
Type of data	Instantaneous value Processed value
Output interval	100 ms
Print out	Printing of measurement results on dedicated printer DPU-414
Power requirements	Four IEC R6 (size AA) batteries (alkaline or rechargeable batteries) or external power supply
Battery life (23 °C)	Alkaline battery LR6 (AA): 26 h NI-MH secondary battery: 25 h At the maximum: * Depends on the setting
AC adapter	NC-98C (NC-34 for previous models cannot be used)
External power voltage	5 to 7 V (rated voltage: 6 V)
Current consumption	Approximately 90 mA (normal operation, rated voltage)
Ambient conditions	Temperature: -10 to +50 °C Humidity: 10 to 90 % RH (non-condensing)
Dustproof / water-resistant performance*4	IP code: IP54 (except for microphone) See precautions regarding waterproofing
Dimensions, weight	Approx. 250 (H) x 76 (W) x 33 mm(D), approx. 400 g (with batteries)
Supplied accessories	Storage case x 1, Windscreen WS-10 x 1, Windscreen fall prevention rubber x 1, Hand strap x 1, LR6 (AA) alkaline batteries x 4, SD card 512 MB x 1 (NX-42EX preinstalled model only)

Options

Product name	Product number
Extended function program (Inst. on 512 MB SD card)	NX-42EX
Waveform recording program*2 (Inst. on 2 GB SD card)	NX-42WR
Octave, 1/3 octave real-time analysis program*2 (Inst. on 512 MB SD card)	NX-42RT
FFT analysis program*2 (Inst. on 512 MB SD card)	NX-42FT
Data management software for environmental measurement	AS-60
Data management software for environmental measurement (Includes the octave and 1/3 octave data management software)	AS-60RT
Waveform analysis software	CAT-WAVE
SD Card 512 MB	SD-512M
SD Card 2 GB	SD-2G
AC adapter (100 V to 240 V)	NC-98C
Battery pack	BP-21
Microphone extension cables	EC-04 (from 2 m)
BNC-Pin output code	CC-24
Comparator output cable	CC-42C
Printer	DPU-414
Printer cable	CC-42P
RS 232C serial I/O cable	CC-42R
USB cable	—
Sound calibrator	NC-74
All-weather windscreen	WS-15
Windscreen mounting adapter	WS-15006
Rain-protection windscreen	WS-1506
Sound level meter tripod	ST-80
All-weather windscreen tripod	ST-81

*1 Use Rion fully guaranteed products. *2 NX-42EX required (sold separately). *3 NX-42WR required (sold separately).
*4 Protection against harmful dust and water splashing from any direction.

Precautions regarding waterproofing

Before use, verify that the rubber bottom cover and the battery compartment lid are firmly closed.
To maintain the water and dust proof rating, internal packing replacement is required every two years (at cost).

* Windows is a trademark of Microsoft Corporation.
* Specifications subject to change without notice.

Distributed by:

This product is environment-friendly. It does not include toxic chemicals on our policy.
This product is certified to an International Protection rating of IP54 (dust protected and resistant to splashing water).
This leaflet is printed with environmentally friendly vegetable-based ink on recycled paper.

1011-4 212 P.D

RION CO., LTD.
http://www.rion.co.jp/english/

3-20-41, Higashimotomachi, Kokubunji, Tokyo 185-8533, Japan
Tel: +81-42-359-7888 Fax: +81-42-359-7442



ISO 14001 RION CO., LTD.
ISO 9001 RION CO., LTD.

Calibration Certificate of Sound Level Meter



中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书

CALIBRATION CERTIFICATE

证书编号: 2HB23001488-0004
Certificate No.



中国认可
国际互认
校准
CALIBRATION
CNAS L13344

委托单位: Castco Testing Centre Limited
Client
仪器名称: Sound Level Meter
Description
型号规格: NL-52
Model/Type
制造商: RION
Manufacturer
机身号: 01287681
Serial No.
管理号: AAST-SLM-12
Asset No.
接收日期: 2023-07-28
Rec. Date
校准日期: 2023-08-07
Cal. Date
签发日期: 2023-08-08
App. Date
建议校准周期: 12个月(12 months)
Reference Cal. Period
结论: 所校准项目符合技术要求(The calibrated items meet the technical requirements)
Conclusion

校准: 赵文钰
Calibrated by
签发: 郑木力
Approved by

核验: 钟灏
Inspected by
印章: Stamp



扫一扫查真伪

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服电话: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Add. of the Lab: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 9 页
Page of

证书编号(Certificate No.): 2HB23001488-0004

说明

DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025:2017标准的要求, 获得中国合格评定国家认可委员会(CNAS) 认可, 认可证书号为: CNAS L13344.
This laboratory quality management system meets the ISO/IEC 17025:2017 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.

2. 本机构出具的数据均可溯源到国际单位制(SI) 单位和社会公用计量标准。
The data issued by this laboratory is traceable to International system of Units (SI) and national primary standards.

3. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
* JJG 188-2017 声级计检定规程: Sound pressure level: (20~130)dB; Frequency Weighting: (20~130)dB, (10 Hz~20kHz)
* 详细内容请查看CNAS网站中注册编号为L13344的证书附件, 超出范围的内容未被认可, 其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)

4. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
实验室标准传声器(2246 093)	GFJGJL1001230304187/2024-04-13/航空304所	$U = (0.05 - 0.20) \text{ dB } (k=2)$	10Hz~20kHz
正弦信号发生器(243165 6)	4GC22000542-0057/2023-10-26/赛宝(广州)	$f: \pm 1 \text{ mHz}$; 失真度: $< -70 \text{ dB}$	$f: 0.001 \text{ Hz} \sim 200 \text{ kHz}$; $U: 100 \mu \text{ V} \sim 5 \text{ Vrms}$
前置放大器(3194482)	4GC22000429-0039/2023-08-29/赛宝(广州)	$\pm 0.1 \text{ dB}$	10Hz~50kHz
数字多用表(MY5300648 3)	4GC22000447-0003/2023-09-26/赛宝(广州)	DCV: $\pm 0.0035\%$; ACV: $\pm 0.06\%$; DCI: $\pm 0.05\%$; ACI: $\pm 0.1\%$; R: $\pm 0.01\%$; $f: \pm 0.001\%$	DCV: (0~1000)V; ACV: (0.001~750)V@3Hz~300kHz; DCI: (0~3)A; ACI: (0~3)A@3Hz~5kHz; R: (0~100)M Ω ; $f: 3 \text{ Hz} \sim 300 \text{ kHz}$
功率放大器(2536312)	4GC22000600-0093/2023-11-30/赛宝(广州)	频率响应: $\pm 1 \text{ dB}$, 失真度: $< 0.2\%$	20Hz~50kHz
PULSE分析系统(3160-1 06540)	4GC23000001-0137/2024-01-03/赛宝(广州)	频率: $U_{\text{ref}}=0.001\%, k=2$; 电压: $U_{\text{ref}}=0.10\%, k=2$	频率: 0.001Hz~51.2kHz; 电压: (1~10) $^{-3}$ ~30V
声校准器(2272351)	4GC22000600-0073/2023-11-29/赛宝(广州)	1级 First Level	31.5Hz~16kHz

5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室

6. 环境条件(Environmental conditions):
温度(Temperature): 25.3°C 相对湿度(Relative Humidity): 65%

7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定, 由合成标准不确定度乘以包含概率约为95%时对应的包含因子 k 得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.

8. 证书中"P"、"合格"代表"测量结果在允许范围内", "F"、"不合格"代表"测量结果不在允许范围内", "N/A"代表"不适用或技术指标暂时无法确认等"。本证书报告的结论仅供参考, 使用人员应结合实际测量的要求合理使用, 如考虑测量结果测量不确定度的影响等。
"P" and "Pass" in this certificate stand for "Low Limit: the measured value $\leq$ High Limit", "F" and "Fail" stand for "the measured value $>$ Low Limit or the measured value $>$ High Limit", "N/A" stands for "Not Applicable or The technical specification has not been confirmed etc". The conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.

第 3 页,共 9 页
Page of

Calibration Certificate of Sound Level Meter

9. 建议校准周期是本实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议, 供委托方参考。委托方可以根据实际使用情况自行决定样品的校准周期。
The reference calibration period is based on the reference documents and normal operating conditions of the calibrated instrument. It is only for reference. The client may decide the calibration period of the instrument according to the actual use.



注: 1. 本证书未经本机构书面授权, 不得部分复制。(The certificate shall not be partly reproduced without written approval of the laboratory.)
2. 本次校准结果仅与被校物有关。(The results are only related to the items calibrated.)
3. “委托方”、“委托方联络信息”由委托方提供, “制造厂”、“型号规格”、“出厂编号”以及“设备编号”为仪器上标注, 委托方对上面内容如有异议, 须在收到证书后二十个工作日内提出。
The information Client and Contact Information are provided by client, and the Manufacturer, Model/Type, Serial No. and Equipment No. are marked on the items. Client shall submit any objection within 20 working days after receiving the certificate for the information above.

第 4 页, 共 9 页
Page of



证书编号(Certificate No.): 2HB23001488-0004

1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中测量结果准确度的因素和缺陷。

There are no factor and defect that affect the measurement result accuracy of the certificate.

2 指示声级调整 (Indication SPL Calibration)

频率(Frequency)=1000Hz

传声器型号 (Microphone Type)	传声器编号 (Microphone SN.)	放大器型号 (Preamplifier Type)	放大器编号 (Preamplifier SN.)	
/	/	/	/	
声校准器型号 (Calibrator Type)	标准声压级 (Reference SPL) (dB)	校准前示值 (Before Calibration) (dB)	校准后示值 (After Calibration) (dB)	U (k=2) (dB)
4226	94.0	94.0	94.0	0.2

3 级线性 (Level Linearity)

3.1 参考级量程 (Reference Range)

频率(Frequency): 8000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
130.0	129.8	-0.2	±0.8	P	0.3
129.0	128.8	-0.2	±0.8	P	0.3
128.0	127.8	-0.2	±0.8	P	0.3
127.0	126.8	-0.2	±0.8	P	0.3
126.0	125.9	-0.1	±0.8	P	0.3
125.0	124.9	-0.1	±0.8	P	0.3
120.0	119.9	-0.1	±0.8	P	0.3
110.0	110.0	0.0	±0.8	P	0.3
100.0	100.0	0.0	±0.8	P	0.3
90.0	90.0	0.0	±0.8	P	0.3
80.0	79.9	-0.1	±0.8	P	0.3
70.0	69.9	-0.1	±0.8	P	0.3
60.0	60.0	0.0	±0.8	P	0.3
50.0	49.9	-0.1	±0.8	P	0.3
40.0	39.9	-0.1	±0.8	P	0.3
35.0	34.8	-0.2	±0.8	P	0.3
34.0	33.8	-0.2	±0.8	P	0.3
33.0	32.9	-0.1	±0.8	P	0.3
32.0	31.8	-0.2	±0.8	P	0.3
31.0	30.8	-0.2	±0.8	P	0.3
30.0	29.8	-0.2	±0.8	P	0.3

数据页(Data sheet) ID: 071288

第 5 页, 共 9 页
Page of

Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB23001488-0004

3.2 其它级量程 (Other Range)

频率(Frequency): 1000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
130.0	129.9	-0.1	±0.8	P	0.3
129.0	128.9	-0.1	±0.8	P	0.3
128.0	127.9	-0.1	±0.8	P	0.3
127.0	126.9	-0.1	±0.8	P	0.3
126.0	125.9	-0.1	±0.8	P	0.3
125.0	124.9	-0.1	±0.8	P	0.3
120.0	120.0	0.0	±0.8	P	0.3
110.0	110.0	0.0	±0.8	P	0.3
100.0	100.0	0.0	±0.8	P	0.3
90.0	90.0	0.0	±0.8	P	0.3
80.0	80.0	0.0	±0.8	P	0.3
70.0	70.0	0.0	±0.8	P	0.3
60.0	60.0	0.0	±0.8	P	0.3
50.0	50.0	0.0	±0.8	P	0.3
40.0	40.0	0.0	±0.8	P	0.3
35.0	34.9	-0.1	±0.8	P	0.3
34.0	33.9	-0.1	±0.8	P	0.3
33.0	32.9	-0.1	±0.8	P	0.3
32.0	31.9	-0.1	±0.8	P	0.3
31.0	30.9	-0.1	±0.8	P	0.3
30.0	29.9	-0.1	±0.8	P	0.3



证书编号(Certificate No.): 2HB23001488-0004

4 A计权特性(A-Weighting Characteristic)

频率 (Frequency) (Hz)	实测值 (Actual) (dB)	理论值 (Theoretical value) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
20	-50.8	-50.5	-0.3	±2.0	P	0.5
25	-45.0	-44.7	-0.3	+2.0 ~ -1.5	P	0.5
31.5	-39.6	-39.4	-0.2	±1.5	P	0.5
40	-34.6	-34.6	0.0	±1.0	P	0.5
50	-30.2	-30.2	0.0	±1.0	P	0.5
63	-26.1	-26.2	0.1	±1.0	P	0.5
80	-22.3	-22.5	0.2	±1.0	P	0.5
100	-19.1	-19.1	0.0	±1.0	P	0.5
125	-16.1	-16.1	0.0	±1.0	P	0.5
160	-13.2	-13.4	0.2	±1.0	P	0.5
200	-10.7	-10.9	0.2	±1.0	P	0.5
250	-8.7	-8.6	-0.1	±1.0	P	0.5
315	-6.8	-6.6	-0.2	±1.0	P	0.4
400	-4.7	-4.8	0.1	±1.0	P	0.4
500	-3.1	-3.2	0.1	±1.0	P	0.4
630	-1.8	-1.9	0.1	±1.0	P	0.4
800	-0.7	-0.8	0.1	±1.0	P	0.4
1000(Ref.)	0.0	0.0	0.0	±0.7	P	0.4
1250	0.6	0.6	0.0	±1.0	P	0.6
1600	1.0	1.0	0.0	±1.0	P	0.6
2000	1.1	1.2	-0.1	±1.0	P	0.6
2500	1.1	1.3	-0.2	±1.0	P	0.6
3150	1.0	1.2	-0.2	±1.0	P	0.6
4000	0.7	1.0	-0.3	±1.0	P	0.6
5000	0.4	0.5	-0.1	±1.5	P	0.6
6300	-0.2	-0.1	-0.1	+1.5 ~ -2.0	P	0.6
8000	-1.0	-1.1	0.1	+1.5 ~ -2.5	P	0.6
10000	-2.3	-2.5	0.2	+2.0 ~ -3.0	P	0.6
12500	-4.2	-4.3	0.1	+2.0 ~ -5.0	P	1.0
16000	-8.5	-6.6	-1.9	+2.5 ~ -16.0	P	1.0
20000	-18.4	-9.3	-9.1	+3.0 ~ -∞	P	1.0

Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB23001488-0004

5 C计权特性(C-Weighting Characteristic)

频率 (Frequency) (Hz)	实测值 (Actual) (dB)	理论值 (Theoretical value) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
20	-6.3	-6.2	-0.1	±2.0	P	0.5
25	-4.5	-4.4	-0.1	+2.0 ~ -1.5	P	0.5
31.5	-3.0	-3.0	0.0	±1.5	P	0.5
40	-2.0	-2.0	0.0	±1.0	P	0.5
50	-1.2	-1.3	0.1	±1.0	P	0.5
63	-0.7	-0.8	0.1	±1.0	P	0.5
80	-0.4	-0.5	0.1	±1.0	P	0.5
100	-0.2	-0.3	0.1	±1.0	P	0.5
125	-0.1	-0.2	0.1	±1.0	P	0.5
160	0.0	-0.1	0.1	±1.0	P	0.5
200	0.0	0.0	0.0	±1.0	P	0.5
250	0.0	0.0	0.0	±1.0	P	0.5
315	0.0	0.0	0.0	±1.0	P	0.4
400	0.0	0.0	0.0	±1.0	P	0.4
500	0.0	0.0	0.0	±1.0	P	0.4
630	0.0	0.0	0.0	±1.0	P	0.4
800	0.0	0.0	0.0	±1.0	P	0.4
1000(Ref.)	0.0	0.0	0.0	±0.7	P	0.4
1250	-0.1	0.0	-0.1	±1.0	P	0.6
1600	-0.2	-0.1	-0.1	±1.0	P	0.6
2000	-0.3	-0.2	-0.1	±1.0	P	0.6
2500	-0.5	-0.3	-0.2	±1.0	P	0.6
3150	-0.8	-0.5	-0.3	±1.0	P	0.6
4000	-1.1	-0.8	-0.3	±1.0	P	0.6
5000	-1.5	-1.3	-0.2	±1.5	P	0.6
6300	-2.1	-2.0	-0.1	+1.5 ~ -2.0	P	0.6
8000	-2.9	-3.0	0.1	+1.5 ~ -2.5	P	0.6
10000	-4.2	-4.4	0.2	+2.0 ~ -3.0	P	0.6
12500	-6.2	-6.2	0.0	+2.0 ~ -5.0	P	1.0
16000	-10.4	-8.5	-1.9	+2.5 ~ -16.0	P	1.0
20000	-20.4	-11.2	-9.2	+3.0 ~ -∞	P	1.0

第 8 页,共 9 页
Page of

数据页(Data sheet) ID: 071288



证书编号(Certificate No.): 2HB23001488-0004

6 自生噪声 (Autogenous noise)

计权 (Weighting)	实测值 (Actual) (dB)
A	17.7

以下空白/No data hereafter



数据页(Data sheet) ID: 071288

第 9 页,共 9 页
Page of

Calibration Certificate of Sound Level Meter

 中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书

CALIBRATION CERTIFICATE

证书编号: 2HB23001488-0003
Certificate No. 

  中国认可
国际互认
校准
CALIBRATION
CNAS L13344

委托单位: Castco Testing Centre Limited
Client

仪器名称: Sound Level Meter
Description

型号规格: NL-52
Model/Type

制造商: RION
Manufacturer

机身号: 00976204
Serial No.

管理号: AAST-SLM-11
Asset No.

接收日期: 2023-07-28
Rec. Date

签发日期: 2023-08-08
App. Date

结论: 所校准项目符合技术要求(The calibrated items meet the technical requirements)
Conclusion

校准: 赵文钰 赵文钰
Calibrated by

检验: 钟灏 钟灏
Inspected by

签发: 郑木力 郑木力
Approved by

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服电话: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Add. of the Lab: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 9 页
Page of

证书编号(Certificate No.): 2HB23001488-0003

说明

DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025:2017标准的要求, 获得中国合格评定国家认可委员会 (CNAS) 认可, 认可证书号为: CNAS L13344。
This laboratory quality management system meets the ISO/IEC 17025:2017 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.
2. 本机构出具的数据均可溯源到国际单位制 (SI) 单位和社会公用计量标准。
The data issued by this laboratory is traceable to International system of Units (SI) and national primary standards.
3. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
 - JJG 188-2017 声级计检定规程: Sound pressure level: (20~130)dB; Frequency Weighting: (20~130)dB, (10 Hz~20kHz)
 - 详细内容请查看CNAS网站中注册编号为L13344的证书附件, 超出范围的内容未被认可, 其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)
4. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
实验室标准传声器(2246 093)	GFJGL1001230304187/2024-04-13/赛宝(广州) 304所	$U=(0.05-0.20)\text{dB} \quad (k=2)$	10Hz~20kHz
正弦信号发生器(243165 6)	4GC22000542-0057/2023-10-26/赛宝(广州)	$f: \pm 1\text{mHz}$ 失真度 Distortion: $< -70\text{dB}$	$f: 0.001\text{Hz} \sim 200\text{kHz}$; $U: 100\mu\text{V} \sim 5\text{Vrms}$
前置放大器(3194482)	4GC22000429-0039/2023-08-29/赛宝(广州)	$\pm 0.1\text{dB}$	10Hz~50kHz
数字多用表(MY5300648 3)	4GC22000447-0003/2023-09-26/赛宝(广州)	DCV: $\pm 0.0035\%$; ACV: $\pm 0.009\%$; DCI: $\pm 0.05\%$; ACI: $\pm 0.1\%$; R: $\pm 0.01\%$; $f: \pm 0.001\%$	DCV: $10 \sim 1000\text{V}$; ACV: $0.001 \sim 750\text{V}$ @ $3\text{Hz} \sim 300\text{kHz}$; DCI: $0 \sim 3\text{A}$; ACI: $0 \sim 3\text{A}$ @ $3\text{Hz} \sim 5\text{kHz}$; R: $0 \sim 100\text{M}\Omega$; $f: 3\text{Hz} \sim 300\text{kHz}$
功率放大器(2536312)	4GC22000600-0093/2023-11-30/赛宝(广州)	频率响应: $\pm 1\text{dB}$, 失真度: $< 0.2\%$	20Hz~50kHz
PULSE分析系统(3160-1 06540)	4GC23000001-0137/2024-01-03/赛宝(广州)	频率: $U_{\text{ref}}=0.001\%$; $k=2$; 电压: $U_{\text{ref}}=0.10\%$; $k=2$	频率: $0.001\text{Hz} \sim 51.2\text{kHz}$; 电压: $(1 \sim 10^3) \sim 30\text{V}$
声校准器(2272351)	4GC22000600-0073/2023-11-29/赛宝(广州)	1级 First Level	31.5Hz~16kHz

5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室
6. 环境条件(Environmental conditions):
温度(Temperature): 25.3°C 相对湿度(Relative Humidity): 65%
7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定, 由合成标准不确定度乘以包含概率约为95%时对应的包含因子 k 得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.
8. 证书中"P"、"合格"代表"测量结果在允许范围内", "F"、"不合格"代表"测量结果不在允许范围内", "N/A"代表"不适用或技术指标暂时无法确认等"。本证书报告的结论仅供参考, 使用人员应结合实际测量的要求合理使用, 如考虑测量结果测量不确定度的影响等。
"P" and "Pass" in this certificate stand for "Low Limit<the measured value<High Limit", "F" and "Fail" stand for "the measured value<Low Limit or the measured value>High Limit", "N/A" stands for "Not Applicable or The technical specification has not been confirmed etc". The conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.

第 3 页,共 9 页
Page of

Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB23001488-0003

1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中测量结果准确度的因素和缺陷。

There are no factor and defect that affect the measurement result accuracy of the certificate.

2 指示声级调整 (Indication SPL Calibration)

频率(Frequency): 1000Hz

传声器型号 (Microphone Type)	传声器编号 (Microphone SN.)	放大器型号 (Preamplifier Type)	放大器编号 (Preamplifier SN.)	
/	/	/	/	
声校准器型号 (Calibrator Type)	标准声压级 (Reference SPL) (dB)	校准前示值 (Before Calibration) (dB)	校准后示值 (After Calibration) (dB)	U (k=2) (dB)
4226	94.0	93.8	93.8	0.2

3 级线性 (Level Linearity)

3.1 参考级量程 (Reference Range)

频率(Frequency): 8000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
130.0	129.8	-0.2	±0.8	P	0.3
129.0	128.8	-0.2	±0.8	P	0.3
128.0	127.8	-0.2	±0.8	P	0.3
127.0	126.8	-0.2	±0.8	P	0.3
126.0	125.9	-0.1	±0.8	P	0.3
125.0	124.9	-0.1	±0.8	P	0.3
120.0	119.9	-0.1	±0.8	P	0.3
110.0	110.0	0.0	±0.8	P	0.3
100.0	100.0	0.0	±0.8	P	0.3
90.0	90.0	0.0	±0.8	P	0.3
80.0	79.9	-0.1	±0.8	P	0.3
70.0	69.9	-0.1	±0.8	P	0.3
60.0	60.0	0.0	±0.8	P	0.3
50.0	49.9	-0.1	±0.8	P	0.3
40.0	39.9	-0.1	±0.8	P	0.3
35.0	34.8	-0.2	±0.8	P	0.3
34.0	33.8	-0.2	±0.8	P	0.3
33.0	32.9	-0.1	±0.8	P	0.3
32.0	31.8	-0.2	±0.8	P	0.3
31.0	30.8	-0.2	±0.8	P	0.3
30.0	29.8	-0.2	±0.8	P	0.3

数据页(Data sheet) ID: 071288

第 5 页,共 9 页
Page of



证书编号(Certificate No.): 2HB23001488-0003

3.2 其它级量程 (Other Range)

频率(Frequency): 1000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
130.0	129.9	-0.1	±0.8	P	0.3
129.0	128.9	-0.1	±0.8	P	0.3
128.0	127.9	-0.1	±0.8	P	0.3
127.0	126.9	-0.1	±0.8	P	0.3
126.0	125.9	-0.1	±0.8	P	0.3
125.0	124.9	-0.1	±0.8	P	0.3
120.0	120.0	0.0	±0.8	P	0.3
110.0	110.0	0.0	±0.8	P	0.3
100.0	100.0	0.0	±0.8	P	0.3
90.0	90.0	0.0	±0.8	P	0.3
80.0	80.0	0.0	±0.8	P	0.3
70.0	70.0	0.0	±0.8	P	0.3
60.0	60.0	0.0	±0.8	P	0.3
50.0	50.0	0.0	±0.8	P	0.3
40.0	40.0	0.0	±0.8	P	0.3
35.0	34.9	-0.1	±0.8	P	0.3
34.0	33.9	-0.1	±0.8	P	0.3
33.0	32.9	-0.1	±0.8	P	0.3
32.0	31.9	-0.1	±0.8	P	0.3
31.0	30.9	-0.1	±0.8	P	0.3
30.0	29.9	-0.1	±0.8	P	0.3

第 6 页,共 9 页
Page of

数据页(Data sheet) ID: 071288

Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB23001488-0003

4 A计权特性(A-Weighting Characteristic)

频率 (Frequency)	实测值 (Actual)	理论值 (Theoretical value)	误差 (Error)	允许误差 (Limit)	结论 (Pass/Fail)	U (k=2)
(Hz)	(dB)	(dB)	(dB)	(dB)	(P/F)	(dB)
20	-50.5	-50.5	0.0	±2.0	P	0.5
25	-44.9	-44.7	-0.2	+2.0 ~ -1.5	P	0.5
31.5	-39.7	-39.4	-0.3	±1.5	P	0.5
40	-34.5	-34.6	0.1	±1.0	P	0.5
50	-30.3	-30.2	-0.1	±1.0	P	0.5
63	-26.2	-26.2	0.0	±1.0	P	0.5
80	-22.3	-22.5	0.2	±1.0	P	0.5
100	-19.1	-19.1	0.0	±1.0	P	0.5
125	-16.1	-16.1	0.0	±1.0	P	0.5
160	-13.2	-13.4	0.2	±1.0	P	0.5
200	-10.8	-10.9	0.1	±1.0	P	0.5
250	-8.6	-8.6	0.0	±1.0	P	0.5
315	-6.6	-6.6	0.0	±1.0	P	0.4
400	-4.7	-4.8	0.1	±1.0	P	0.4
500	-3.2	-3.2	0.0	±1.0	P	0.4
630	-1.9	-1.9	0.0	±1.0	P	0.4
800	-0.8	-0.8	0.0	±1.0	P	0.4
1000(Ref)	0.0	0.0	0.0	±0.7	P	0.4
1250	0.5	0.6	-0.1	±1.0	P	0.6
1600	0.9	1.0	-0.1	±1.0	P	0.6
2000	1.1	1.2	-0.1	±1.0	P	0.6
2500	1.1	1.3	-0.2	±1.0	P	0.6
3150	0.9	1.2	-0.3	±1.0	P	0.6
4000	0.7	1.0	-0.3	±1.0	P	0.6
5000	0.3	0.5	-0.2	±1.5	P	0.6
6300	-0.2	-0.1	-0.1	+1.5 ~ -2.0	P	0.6
8000	-1.1	-1.1	0.0	+1.5 ~ -2.5	P	0.6
10000	-2.3	-2.5	0.2	+2.0 ~ -3.0	P	0.6
12500	-4.3	-4.3	0.0	+2.0 ~ -5.0	P	1.0
16000	-8.5	-6.6	-1.9	+2.5 ~ -16.0	P	1.0
20000	-18.4	-9.3	-9.1	+3.0 ~ -∞	P	1.0

数据页(Data sheet) ID: 071288

第 7 页,共 9 页
Page of



证书编号(Certificate No.): 2HB23001488-0003

5 C计权特性(C-Weighting Characteristic)

频率 (Frequency)	实测值 (Actual)	理论值 (Theoretical value)	误差 (Error)	允许误差 (Limit)	结论 (Pass/Fail)	U (k=2)
(Hz)	(dB)	(dB)	(dB)	(dB)	(P/F)	(dB)
20	-6.6	-6.2	-0.4	±2.0	P	0.5
25	-4.7	-4.4	-0.3	+2.0 ~ -1.5	P	0.5
31.5	-3.0	-3.0	0.0	±1.5	P	0.5
40	-2.0	-2.0	0.0	±1.0	P	0.5
50	-1.3	-1.3	0.0	±1.0	P	0.5
63	-0.8	-0.8	0.0	±1.0	P	0.5
80	-0.4	-0.5	0.1	±1.0	P	0.5
100	-0.2	-0.3	0.1	±1.0	P	0.5
125	-0.1	-0.2	0.1	±1.0	P	0.5
160	0.0	-0.1	0.1	±1.0	P	0.5
200	0.0	0.0	0.0	±1.0	P	0.5
250	0.0	0.0	0.0	±1.0	P	0.5
315	0.0	0.0	0.0	±1.0	P	0.4
400	0.0	0.0	0.0	±1.0	P	0.4
500	0.0	0.0	0.0	±1.0	P	0.4
630	0.0	0.0	0.0	±1.0	P	0.4
800	0.0	0.0	0.0	±1.0	P	0.4
1000(Ref)	0.0	0.0	0.0	±0.7	P	0.4
1250	-0.1	0.0	-0.1	±1.0	P	0.6
1600	-0.2	-0.1	-0.1	±1.0	P	0.6
2000	-0.3	-0.2	-0.1	±1.0	P	0.6
2500	-0.5	-0.3	-0.2	±1.0	P	0.6
3150	-0.8	-0.5	-0.3	±1.0	P	0.6
4000	-1.1	-0.8	-0.3	±1.0	P	0.6
5000	-1.5	-1.3	-0.2	±1.5	P	0.6
6300	-2.1	-2.0	-0.1	+1.5 ~ -2.0	P	0.6
8000	-3.0	-3.0	0.0	+1.5 ~ -2.5	P	0.6
10000	-4.3	-4.4	0.1	+2.0 ~ -3.0	P	0.6
12500	-6.2	-6.2	0.0	+2.0 ~ -5.0	P	1.0
16000	-10.4	-8.5	-1.9	+2.5 ~ -16.0	P	1.0
20000	-20.3	-11.2	-9.1	+3.0 ~ -∞	P	1.0

第 8 页,共 9 页
Page of

数据页(Data sheet) ID: 071288

Catalogue of Sound Calibrator

For microphone calibration NC-74

How to use

Carefully insert the microphone all the way into the coupler of the NC-74. Then simply turn the power on to apply a constant sound pressure level to the diaphragm of the microphone.




Usage example (NL series)

The performance of the NC-74 is suitable for calibration of high-precision sound level meters. The unit is compact, lightweight, and easy to use. Two IEC LR6 (size AA) alkaline batteries will power the unit for more than 30 hours of continuous use at room temperature.

Atmospheric pressure compensation principle

The NC-74 incorporates a sensor that detects atmospheric pressure. Based on the information provided by the sensor, the CPU controls the signal amplitude. This allows the unit to always provide the correct output for achieving constant sound pressure level, regardless of fluctuations in atmospheric pressure.

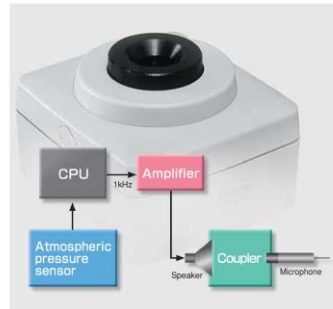

Using the 1/2-inch adapter

To allow calibration of sound level meter microphones with 1 inch diameter, the 1/2-inch microphone adapter can be removed. 1/2-inch microphones are calibrated with the adapter in place.



Specifications

Applicable standards	IEC 60942:2003 Class 1 JIS C 1515:2004 Class 1
Suitable microphones	1-inch microphones IEC 61094-1 Type LS1P UC-27 UC-25 UC-34 1/2-inch microphones IEC 61094-1 Type LS2aP UC-59 UC-57 UC-56A UC-52 UC-56 UC-30 UC-31 UC-38P
Nominal sound pressure level	94 dB
Sound pressure level tolerance	±0.3 dB
Nominal frequency	1 kHz
Frequency tolerance	±1.0 % or less
Power requirements	IEC LR6 (size AA) alkaline battery × 2
Dimensions, mass	Approx. 49 (H) × 80 (W) × 74 (D) mm Approx. 200 g (including batteries)
Supplied accessories	Case X-1 IEC LR6 (size AA) alkaline battery × 2 1/2-inch microphone adapter NC-74-002 X-1

* Specification subject to change without notice.

RION CO., LTD.

3-20-41, Higashimotomachi, Kokubunji, Tokyo 185-8533, Japan
Tel: +81-42-359-7888 Fax: +81-42-359-7442
<http://www.rion.co.jp/english/>

Distributed by:

ISO 14001 RION CO., LTD.
ISO 9001 RION CO., LTD.



Printed in Japan 0510-1 0807.P.M.P




Usage example

How to use the adapter

1-inch microphones

To use the sound calibrator with 1-inch diameter microphones, remove the 1/2-inch microphone adapter.



1/2-inch microphones

To use the sound calibrator with 1/2-inch diameter microphones, the supplied 1/2-inch microphone adapter must be in place.



Make sure the 1/2-inch adapter is locked.

1/4-inch microphones

To use the sound calibrator with 1/4-inch diameter microphones, use the supplied 1/2-inch microphone adapter together with the optional 1/4-inch adapter.



Specifications (under standard ambient conditions*)

Applicable standards	IEC 60942:2017 class 1, ANSI S1.40-2008 class 1, JIS C 1515:2004 class 1, CE marking, WEEE directive, Chinese RoHS
Supported microphones	Microphones made by RION and microphones made by other manufacturers that meet the IEC 61094-4 size specifications 1-inch microphones 1/2-inch microphones (with supplied adapter) 1/4-inch microphones (with optional adapter)
Nominal sound pressure level	94 dB
Sound pressure level tolerance	Max. ±0.3 dB
Operational frequency	1,000 Hz
Frequency tolerance	Max. ±0.5%
THD + noise	Max. 1.0 % (22.4 Hz to 22.4 kHz)
Dimensions and weight	Approx. 42 mm (H) × 77 mm (W) × 30 mm (D), approx. 200 g
Power supply	IEC LR6 (size AA) alkaline battery × 2 IEC LR6 (size AA) nickel-hybrid rechargeable battery (1-envelop pin*) supported × 2
Battery life	40 hours of active duty (two alkaline batteries, continuous use) 50 hours or more (using two nickel-hybrid rechargeable batteries (envelop pin), continuous use)
Supplied accessories	Soft case X-1, 1/2-inch microphone adapter X-1, IEC LR6 (size AA) alkaline battery × 2, hand strap X-1, JC55 Calibration Certificate X-1
* RION standard ambient conditions: static pressure 101.325 kPa, ambient temperature 23 °C, relative humidity 50 %	
Optional accessories	1/4-inch microphone adapter NC-75-S11

Strap



Securely carry the unit with the supplied hand strap.

Soft case



Calibration can be performed with the calibrator inserted in the soft case.

PISTONPHONE NC-72A

Applicable standards	IEC 60942:2017 class 1 S/A, class 1 A, JIS C 1515:2004 class 1 S/C, class 1 C
Nominal sound pressure level	114 dB, Sound pressure level tolerance ±0.3 dB



RION CO., LTD. is recognized by the JCSS which uses ISO/IEC 17025 as an accreditation standard and issues its accreditation scheme on G03/B/C 17011. JCSS is operated by the accreditation body (UK) which is a regulatory body for the Quality Assurance of Calibration Services (UKAS). The Quality Assurance of Calibration Services (UKAS) is an international body compliant with the accreditation standard, ISO/IEC 17025.

* Windows is a trademark of Microsoft Corporation. * Specifications subject to change without notice.

Distributed by:

RION CO., LTD.

<https://rion-sv.com/>

3-20-41, Higashimotomachi, Kokubunji, Tokyo 185-8533, Japan
Tel: +81-42-359-7888 Fax: +81-42-359-7442

This product is environment-friendly. It does not include toxic chemicals on our policy.
This wallet is printed with environmentally friendly UV ink.

1709-E (016)PG

Calibration Certificate of Sound Calibrator

CAL: 5 Sep 2023 AAST-SLC-07



中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书 CALIBRATION CERTIFICATE

证书编号: 2HB23001715-0002
Certificate No. 




中国认可
国际互认
校准
CALIBRATION
CNAS L13344

委托单位: Client	Castco Testing Centre Limited		
仪器名称: Description	Sound Level Calibrator		
型号规格: Model/Type	NC-75		
制造商: Manufacturer	RION		
机身号: Serial No.	34280310		
管理号: Asset No.	AAST-SLC-07		
接收日期: Rec. Date	2023-08-23	校准日期: Cal. Date	2023-09-05
签发日期: App. Date	2023-09-05	建议校准周期: Reference Cal. Period	12个月(12 months)
结论: Conclusion	所校准项目符合技术要求(The calibrated items meet the technical requirements)		

校准:
Calibrated by 赵文钰 赵文钰

签发:
Approved by 郑木力 郑木力

核验:
Inspected by 钟灏 钟灏

印章:
Stamp



扫一扫查真伪

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服电话: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhaocun Avenue West,Zengcheng District,Guangzhou,China
Add. of the Lab: No.78,Zhaocun Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 5 页
Page of

证书编号(Certificate No.): 2HB23001715-0002

说明 DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025:2017标准的要求, 获得中国合格评定国家认可委员会 (CNAS) 认可, 认可证书号为: CNAS L13344.
This laboratory quality management system meets the ISO/IEC 17025:2017 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.
2. 本机构出具的数据均可溯源到国际单位制 (SI) 单位和社会公用计量标准。
The data issued by this laboratory is traceable to International system of Units (SI) and national primary standards.
3. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
 - JJG 176-2022 声校准器检定规程: Sound Pressure Level: 94dB、104dB、114dB、124dB(63Hz~8kHz); 94dB、104dB、114dB,(31.5Hz~16kHz); Frequency: 31.5Hz~16kHz; Harmonic Distortion: 0.1%~10%, (20Hz~20kHz)
 - 详细内容请查看CNAS网站中注册编号为L13344的证书附件, 超出范围的内容未获认可, 其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)
4. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
实验室标准声源(2246 093)	GFJJL1001230304187/2024-04-13/航空304所	LS8级	10Hz~25kHz
前置放大器(2239843)	GFJJL1001230304185/2024-03-22/航空304所	频率响应: $\pm 0.1\text{dB}$	(10~50000) Hz
数字多用表(MY4505167 4)	GFJJL1004230400378/2024-04-02/航天514所	DCV: $\pm 8 \times 10^{-5}$; DCI: $\pm 2 \times 10^{-5}$; ACV: $\pm 0.02\%$; ACI: $\pm 0.03\%$; R: $\pm 1 \times 10^{-3}$; $\pm 0.01\%$	DCV: 10mV~1000V; DCI: 1pA~1A; ACV: (10mV~700V) @ (1Hz~2MHz); ACI: (100pA~1A) @ (10Hz~100kHz); R: 10pΩ~1GΩ; F: 1Hz~10MHz
PULSE分析系统(3160-1 06540)	4GC23000528-0009/2024-08-16/赛宝(广州)	频率: $U_{100}=0.001\%$; $k=2$; 电压: $U_{100}=0, 10\%$; $k=2$	频率: 0.001Hz~51.2kHz; 电压: (1~10 ⁻² ~30)V
5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室
6. 环境条件(Environmental conditions):
温度(Temperature): 21.2°C 相对湿度(Relative Humidity): 60%
7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定, 由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.
8. 证书中"P"、"合格"代表"测量结果在允许范围内", "F"、"不合格"代表"测量结果不在允许范围内", "N/A"代表"不适用或技术指标暂时无法确认等"。本证书报告的结论仅供参考, 使用人员应结合实际测量的要求合理使用, 如考虑测量结果测量不确定度的影响等。
"P" and "Pass" in this certificate stand for "Low Limit≤the measured value≤High Limit", "F" and "Fail" stand for "the measured value<Low Limit or the measured value>High Limit", "N/A" stands for "Not Applicable or the technical specification has not been confirmed etc". The conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.
9. 建议校准周期是实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议, 供委托方参考。委托方可以根据实际使用情况自行决定样品的校准周期。

第 3 页,共 5 页
Page of

Calibration Certificate of Sound Calibrator

CEPREI 证书编号(Certificate No.): 2HB23001715-0002

1 外观与工作正常性检查 (Appearance and Function Check)
无影响证书中测量结果准确度的因素和缺陷。
There are no factor and defect that affect the measurement result accuracy of the certificate.

2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	接受限 (Limit)	结论 (Pass/Fail)	U (dB)
94 (dB)	93.90 (dB)	0.10 (dB)	≤0.25 (dB)	P	0.10 (dB)

3 频率 (Frequency)

规定频率 (Prescribed Fre.)	测量频率 (Measured Fre.)	频率误差的绝对值 (Absolute value of Fre.)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (%)
1000 (Hz)	1000.0 (Hz)	0.00 (%)	≤0.70 (%)	P	0.10 (%)

4 总失真+噪声 (Distortion and noise)

规定声压级 (Prescribed SPL)	规定频率 (Measured Fre.)	总失真+噪声 (Distortion and noise)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (%)
94 (dB)	1000 (Hz)	0.60 (%)	≤2.50 (%)	P	5.0 (%)

以下空白/No data hereafter

CEPREI

数据页(Data sheet) ID: 013393 第 5 页,共 5 页
Page of

CEPREI 中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书 CALIBRATION CERTIFICATE

证书编号: 2HB23001715-0001
Certificate No. 

 中国认可
国际互认
校准
CALIBRATION
CNAS L13344

委托单位: Castco Testing Centre Limited
Client

仪器名称: Sound Level Calibrator
Description

型号规格: NC-74
Model/Type

制造商: RION
Manufacturer

机身号: 34678556
Serial No.

管理号: AAST-SLC-06
Asset No.

接收日期: 2023-08-23
Rec. Date

校准日期: 2023-09-05
Cal. Date

签发日期: 2023-09-05
App. Date

建议校准周期: 12个月(12 months)
Reference Cal. Period

结论: 所校准项目符合技术要求(The calibrated items meet the technical requirements)
Conclusion

CEPREI

校准: 赵文钰 赵文钰
Calibrated by

检验: 钟瀚 钟瀚
Inspected by

签发: 郑木力 郑木力
Approved by

印章: 
Stamp

 扫一扫查真伪

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服电话: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Add. of the Lab: No.78,Zhuocun Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 5 页
Page of

Calibration Certificate of Sound Calibrator

证书编号(Certificate No.): 2HB23001715-0001

说明 DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025:2017标准的要求, 获得中国合格评定国家认可委员会 (CNAS) 认可, 认可证书号为: CNAS L13344。
This laboratory quality management system meets the ISO/IEC 17025:2017 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.

2. 本机构出具的数据均可溯源到国际单位制 (SI) 单位和社会公用计量标准。
The data issued by this laboratory is traceable to International system of Units (SI) and national primary standards.

3. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
* JJG 176-2022 声校准器检定规程: Sound Pressure Level: 94dB、104dB、114dB、124dB(63Hz~8kHz); 94dB、104dB、114dB、(31.5Hz~16kHz); Frequency: 31.5Hz~16kHz; Harmonic Distortion: 0.1%~10%, (20Hz~20kHz)
* 详细内容请查看CNAS网站中注册编号为L13344的证书附件。超出范围的内容未被认可, 其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)

4. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):

名称 (Description)	证书号/有效期至/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
前置放大器(2239843)	GFJGJL1001230304185/2024-03-22/航空304所	频率响应: ± 0.1 dB	(10~50000) Hz
数字多用表(MY45051674)	GFJGJL1004230400378/2024-04-02/航天514所	DCV: $\pm 8 \times 10^{-5}$; DCI: $\pm 2 \times 10^{-5}$; ACV: $\pm 0.02\%$; ACI: $\pm 0.03\%$; R: $\pm 1 \times 10^{-3}$; f: $\pm 0.01\%$	DCV: 10nV~1000V; DCI: 1pA~1A; ACV: (10nV~700V) @ (1Hz~2MHz); ACI: (100pA~1A) @ (10Hz~100kHz); R: 10 $\mu\Omega$ ~1G Ω ; f: 1Hz~10MHz
PULSE分析系统(3160-106540)	4GC23000528-0009/2024-08-16/赛宝(广州)	频率: $U_{rel}=0.001\%$; A=2; 电压: $U_{rel}=0.10\%$; A=2	频率: 0.001Hz~51.2kHz; 电压: $(1 \times 10^{-7} \sim 30)$ V
实验室标准传声器(2246093)	GFJGJL1001230304187/2024-04-13/航空304所	LS级	10Hz~25kHz

5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室

6. 环境条件(Environmental conditions):
温度(Temperature): 21.2°C 相对湿度(Relative Humidity): 60%

7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定, 由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.

8. 证书中"P"、"合格"代表"测量结果在允许范围内", "F"、"不合格"代表"测量结果不在允许范围内", "N/A"代表"不适用或技术指标暂时无法确认等"。本证书报告的结论仅供参考, 使用人员应结合实际测量的要求合理使用, 如考虑测量结果测量不确定度的影响等。
"P" and "Pass" in this certificate stand for "Low Limit: the measured value $\leq$ High Limit", "F" and "Fail" stand for "the measured value > Low Limit or the measured value > High Limit", "N/A" stands for "Not Applicable or The technical specification has not been confirmed etc". The conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.

9. 建议校准周期是为本实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议, 供委托方参考。委托方可以根据实际使用情况自行决定样品的校准周期。

第 3 页, 共 5 页
Page of

证书编号(Certificate No.): 2HB23001715-0001

1 外观与工作正常性检查 (Appearance and Function Check)
无影响证书中测量结果准确度的因素和缺陷。
There are no factor and defect that affect the measurement result accuracy of the certificate.

2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	接受限 (Limit)	结论 (Pass/Fail)	U (k=2)
(dB)	(dB)	(dB)	(dB)		(dB)
94	93.86	0.14	≤ 0.25	P	0.10

3 频率 (Frequency)

规定频率 (Prescribed Fre.)	测量频率 (Measured Fre.)	频率误差的绝对值 (Absolute value of Fre.)	接受限 (Limit)	结论 (Pass/Fail)	U _{rel} (k=2)
(Hz)	(Hz)	(%)	(%)		(%)
1000	1003.7	0.37	≤ 0.70	P	0.10

4 总失真+噪声 (Distortion and noise)

规定声压级 (Prescribed SPL)	规定频率 (Measured Fre.)	总失真+噪声 (Distortion and noise)	接受限 (Limit)	结论 (Pass/Fail)	U _{rel} (k=2)
(dB)	(Hz)	(%)	(%)		(%)
94	1000	0.69	≤ 2.50	P	5.0

以下空白/No data hereafter

数据页(Data sheet) ID: 013393 第 5 页, 共 5 页
Page of

Catalogue of Air Flow Meter (TSI TA440)

SPECIFICATIONS

THERMAL ANEMOMETERS MODELS TA410, TA430 AND TA440

Velocity

Range (TA410)	0 to 20 m/s (0 to 4,000 ft/min)
Range (TA430, TA440)	0 to 30 m/s (0 to 6,000 ft/min)
Accuracy (TA410) ^{1,2}	±5% of reading or ±0.025 m/s (±5 ft/min), whichever is greater
Accuracy (TA430, TA440) ^{1,2}	±3% of reading or ±0.015 m/s (±3 ft/min), whichever is greater
Resolution	0.01 m/s (1 ft/min)

Duct Size (TA430, TA440)

Dimensions	1 to 635 cm in increments of 0.1 cm (1 to 250 inches in increments of 0.1 in.)
------------	--

Volumetric Flow Rate (TA430, TA440)

Range	Actual range is a function of velocity, and duct size
-------	---

Temperature

Range (TA410, TA430)	-18 to 93°C (0 to 200°F)
Range (TA440)	-10 to 60°C (14 to 140°F)
Accuracy ³	±0.3°C (±0.5°F)
Resolution	0.1°C (0.1°F)

Relative Humidity (TA440 only)

Range	5 to 95% RH
Accuracy ⁴	±3% RH
Resolution	0.1% RH

Wet Bulb Temperature (TA440 only)

Range	5 to 60°C (40 to 140°F)
Resolution	0.1°C (0.1°F)

Dew Point (TA440 only)

Range	-15 to 49°C (5 to 120°F)
Resolution	0.1°C (0.1°F)

Instrument Temperature Range

Operating (Electronics)	5 to 45°C (40 to 113°F)
Model TA410, TA430	-18 to 93°C (0 to 200°F)
Operating (Probe)	-10 to 60°C (14 to 140°F)
Model TA440	-10 to 60°C (14 to 140°F)
Operating (Probe)	-20 to 60°C (-4 to 140°F)
Storage	-20 to 60°C (-4 to 140°F)

Data Storage Capabilities (TA430, TA440)

Range	12,700+ samples and 100 test IDs
-------	----------------------------------

Logging Interval (TA430, TA440)

1 second to 1 hour

Specifications subject to change without notice.

TSI and the TSI logo are registered trademarks, and Airflow, the Airflow logo and LogDat2 are trademarks of TSI Incorporated.



Airflow Instruments, TSI Instruments Ltd.
Visit our website at www.airflowinstruments.co.uk for more information.

UK Tel: +44 140 4 459200 Germany Tel: +49 241 523030
France Tel: +33 491 11 87 64

P/N 29805-48 Rev D (A4) ©2014 TSI Incorporated

Time Constant (TA430, TA440)

User selectable

External Meter Dimensions

8.4 cm x 17.8 cm x 4.4 cm (3.3 in. x 7.0 in. x 1.8 in.)

Meter Weight with Batteries

0.27 kg (0.6 lbs.)

Meter Probe Dimensions

Probe Length	101.6 cm (40 in.)
Probe Diameter of Tip	7.0 mm (0.28 in.)
Probe Diameter of Base	13.0 mm (0.51 in.)

Articulating Probe Dimensions

Articulating Section Length	19.7 cm (7.8 in.)
Diameter of Articulating Knuckle	9.5 mm (0.38 in.)

Power Requirements

Four AA-size batteries or AC adapter

	TA410	TA430 TA430-A	TA440 TA440-A
Velocity range 0 to 20.00 m/s (0 to 4000 ft/min)	+		
Velocity range 0 to 30.00 m/s (0 to 6000 ft/min)		+	+
Temperature	+	+	+
Flow		+	+
Humidity, wet bulb, dew point			+
Probe	Straight	Straight or -A articulated	Straight or -A articulated
Variable time constant		+	+
Manual data logging		+	+
Auto save data logging			+
Statistics		+	+
Review data		+	+
LogDat2 downloading software		+	+
Free Certificate of Calibration	+	+	+

¹Temperature compensated over an air temperature range of 5 to 65°C (40 to 150°F).

²The accuracy statement begins at 30 ft/min through 4000 ft/min (0.15 m/s through 20 m/s) for the Model TA410, and 30 ft/min through 6000 ft/min (0.15 m/s through 30 m/s) for Models TA430 and TA440.

³Accuracy with instrument case at 25°C (77°F), add uncertainty of 0.03°C/°C (0.05°F/°F) for change in instrument temperature.

⁴Accuracy with probe at 25°C (77°F). Add uncertainty of 0.2% RH/°C (0.1% RH/°F) for change in probe temperature. Includes 1% hysteresis.

Calibration Certificate of Air Flow Meter



Cal Lab Limited 校正實驗室有限公司

Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
Tsuen Wan, NT, Hong Kong
Tel: +852 25680106 Email: info@callab.com.hk
Fax: +852 30116194 Website: www.callab.com.hk



Calibration Certificate No.: CC0242312

Information provided by customer

Customer: Castco Testing Centre Limited
Address: 33, On Kui Street, Fanling, N.T.

Equipment identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Air Velocity Monitor	TSI	AIRFLOW TA440	TA4401232005	AAS-Flow-02

Certificate Information

Date of Receipt:	15 December 2023	Calibration Condition:	21.3°C, 56%RH, 1014hPa
Date of Calibration:	18 December 2023	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	SOP-112	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Hot Wire Anemometer	9535	T93351316004	11 August 2024

Result of Calibration

Reference Reading (m/s)	Measured Reading (m/s)	Error (m/s)	Uncertainty (%)	Technical Requirement	Technical Reference Doc.
0.99	0.99	0.00	3.6	± 5 %	Mfr's Spec.
2.02	2.03	0.01	3.6	± 5 %	Mfr's Spec.
5.01	4.98	-0.03	3.6	± 5 %	Mfr's Spec.
7.96	8.07	0.11	3.6	± 5 %	Mfr's Spec.

CT-AIR-01

Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognised standard and are calibrated on a schedule to maintain the accuracy and good condition.

Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.

Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.

Calibrated By:

Wing Cheng

Checked and Approved By:

Warren Yeung

Company Chop:



Certificate Issue Date: 19 December 2023

CT-REG-04

*** End of Certificate ***

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
- The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0242312

Page 1 of 1

Appendix L – Noise monitoring results and graphical presentation

M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop


Date	Temp (°C)	Weather	Measured Noise Level at M11, dB(A)							Limit
			Time			Baseline	L _{Aeq}	L _{A10}	L _{A90}	
05/07/2024	33.1	Sunny	15:11	-	15:41	68.3	73.2	77.6	65.9	75
11/07/2024	33.8	Cloudy	9:57	-	10:27	68.3	72.4	76.3	66.2	75
17/07/2024	32.6	Cloudy	14:07	-	14:37	68.3	73.6	78.2	66.9	75
23/07/2024	35.2	Sunny	10:34	-	11:04	68.3	72.7	77.1	65.3	75
29/07/2024	28.9	Cloudy	13:28	-	13:58	68.3	71.6	75.7	65.1	75
Maximum						73.6				
Minimum						71.6				
Average						72.8				

NOTE: Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 30-min noise monitoring at M11 were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for M11 is confirmed.

M12 - Hong Kong Children's Hospital


Date	Temp (°C)	Weather	Measured Noise Level at M12, dB(A)							Limit
			Time			Baseline	L _{Aeq}	L _{A10}	L _{A90}	
05/07/2024	33.1	Sunny	10:34	-	11:04	61.9	62.4	63.9	59.4	75
11/07/2024	33.8	Cloudy	14:42	-	15:12	61.9	63.4	64.5	60.1	75
17/07/2024	32.6	Cloudy	10:21	-	10:51	61.9	64.7	68.5	60.5	75
23/07/2024	35.2	Sunny	14:36	-	15:06	61.9	63.3	64.4	59.6	75
29/07/2024	28.9	Cloudy	10:28	-	10:58	61.9	62.4	64.5	60.1	75
Maximum						64.7				
Minimum						62.4				
Average						63.3				

L_{Aeq}, 30-min graphical results of M11 - The Hong Kong Society for the Blind's Factory cum Sheltered Workshop

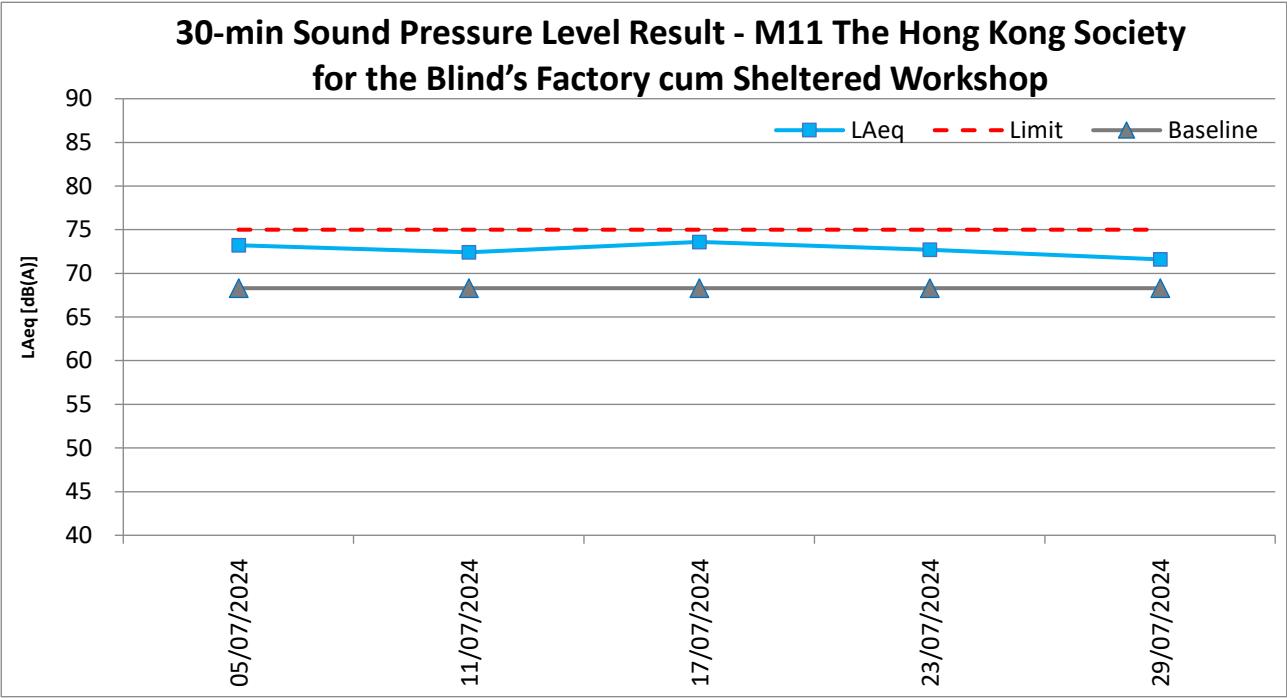

NOTE: Due to the relocation of The Hong Kong Society for the Blind's Factory cum Sheltered Workshop (M11), the premises owner rejected ET to conduct impact monitoring since 1 Sept 2022. 30-min noise monitoring at M11 were conducted on the ground floor with orienting to the Project site. ET will resume the impact monitoring once the alternative monitoring location for M11 is confirmed.

L_{Aeq}, 30-min graphical results of M12 - Hong Kong Children's Hospital

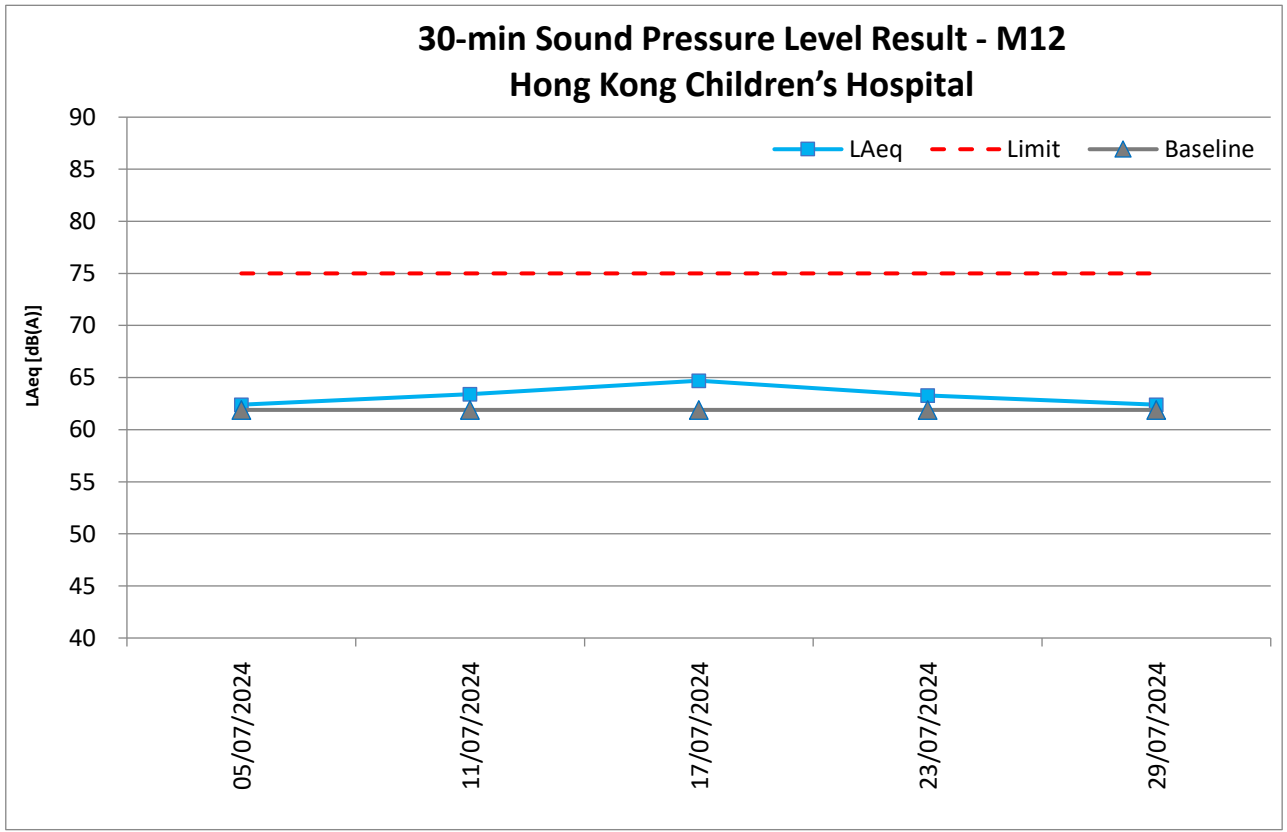

Appendix M – Event and Action Plan for noise

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded	1. Notify Supervisor / ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, Supervisor / ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures submitted by the Contractor and advise the ER accordingly; 3. Advise the Supervisor / ER on the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Submit noise mitigation proposal to IEC and Supervisor / ER; 2. Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified.)
Limit Level being exceeded	1. Inform IEC, Supervisor /ER, Contractor and EPD; 2. Repeat measurement to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedure; 6. Discuss remedial measures required with the IEC, Contractor and Supervisor /ER; 7. Assess effectiveness of	1. Discuss the potential remedial actions with Supervisor /ER, ET and Contractor; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and Supervisor /ER within 3 working days of notification; 3. Implement the agreed proposal; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated. (The above actions should be

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	Contractor's remedial actions and keep IEC, EPD, and Supervisor /ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified.)		exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified.)	taken within 2 working days after the exceedance is identified.)

Appendix N – Event and Action Plan for Landscape and Visual Impact

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Design Check	1. Check final design conforms to the requirements of EP and prepare report.	1. Check report. 2. Recommend remedial design if necessary.	1. Undertake remedial design if necessary.	
Non-conformity on one occasion	1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 4. Monitor remedial actions until rectification has been completed.	1. Check report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Check implementation of remedial measures.	1. Notify Contractor. 2. Ensure remedial measures are properly implemented.	1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.
Repeated Non-conformity	1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Increase monitoring frequency. 4. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 5. Monitor remedial actions until rectification has been completed. 6. If non-conformity stops, cease additional monitoring.	1. Check monitoring report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Notify Contractor. 2. Ensure remedial measures are properly implemented.	1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.

Appendix O – Waste Flow Table

Appendix I - Monthly Summary Waste Flow Table

Name of Department: CEDD

Contract No.: ED/2018/01

Monthly Summary Waste Flow Table for July 2024

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m³)
Jan	2.311	0.111	--	--	2.311	--	--	--	--	--	0.184
Feb	2.232	0.177	--	--	2.232	--	--	--	--	--	0.173
Mar	2.893	0.032	--	--	2.893	--	--	0.051	--	--	0.259
Apr	3.482	0.016	--	--	3.482	--	--	--	--	--	0.238
May	5.531	0.595	--	--	5.531	--	--	--	--	--	0.143
Jun	1.610	0.248	--	--	1.610	1.106	--	--	--	--	0.190
Sub-total	18.059	1.179	--	--	18.059	1.106	--	0.051	--	--	1.187
July	2.088	0.199	--	--	2.088	6.397	--	--	--	--	0.301
Aug											
Sep											
Oct											
Nov											
Dec											
Total	20.147	1.378	--	--	20.147	7.503	--	0.051	--	--	1.488
Forecast of Total Quantities of C&D Materials to be Generated from the Contract*											
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse	
(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m³)	
207.384	2.103	10.2	140	27.415	25	200	0.8	0.1	--	3.891	

- Notes:
- (1) The performance targets are given in **ER Appendix 8I Clause 14** and the EM&A Manual
 - (2) The waste flow table shall also include C&D materials to be imported for use at the Site
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and water barrier
 - (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000m³ (**ER Part 8 Clause 8.7.5(d)(ii)** refers)
 - (5) Assume inert C&D materials density and non-inert C&D materials are 1.9 ton/m³ and 1.5 ton/m³

Appendix P – Environmental Mitigation Implementation Schedule (EMIS)

Implementation Schedule for Air Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.2		8 times daily watering of the work site with active dust emitting activities.	^
S3.2	S4.8	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimize cumulative dust impacts.	^
		- Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.	^*
		- Misting for the dusty material should be carried out before being loaded into the vehicle.	^
		- Any vehicle with an open load carrying area should have properly fitted side and tail boards.	^
		- Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.	^
		- The tarpaulin should be properly secured and should extent at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary, before transportation.	^
		- The vehicles should be restricted to maximum speed of 10 km per hour and confined haulage and delivery vehicle to designated roadways insider the site. On- site unpaved roads should be compacted and kept free of lose materials.	^
		- Vehicle washing facilities should be provided at every vehicle exit point.	^
		- The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	^
		- Every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.	^*
		- Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the three sides.	^
		- Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.	^

Implementation Schedule for Noise Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.3		Use of quiet PME, movable barriers for Asphalt Paver, Breaker, Excavator and Hand-held breaker and full enclosure for Air Compressor, Bar Bender, Concrete Pump, Generator and Water Pump.	^
S3.3		Good Site Practice:	
S3.3		- Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.	^*
		- Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program.	^
		- Mobile plant, if any, should be sited as far away from NSRs as possible.	^
		- Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.	^
		- Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	^
		- Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.	^
		- Scheduling of Construction Works during School Examination Period	N/A

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.4		<u>Construction Runoff</u> Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include:	^
S3.4		- use of sediment traps.	^
S3.4		- adequate maintenance of drainage systems to prevent flooding and overflow.	^

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
	S5.8	- Surface run-off from construction sites should be discharged into storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sedimentation basins.	^
	S5.8	- Channels or earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels should be provided on site boundaries where necessary to intercept storm run-off from outside the site so that it will not wash across the site. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	^
	S5.8	- Silt removal facilities, channels and manholes should be maintained and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to prevent local flooding. Any practical options for the diversion and re-alignment of drainage should comply with both engineering and environmental requirements in order to provide adequate hydraulic capacity of all drains. Minimum distance of 100 m should be maintained between the discharge points of construction site run-off and the existing saltwater intakes.	^
	S5.8	- Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	^
	S5.8	- Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	^
	S5.8	- Open stockpiles of construction materials (e.g. aggregates, sand and fill material) on sites should be covered with tarpaulin or similar fabric during rainstorms.	^
	S5.8	- Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul	^

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		sewerage system.	
	S5.8	- Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	^
S3.4		Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	^
S3.4	S5.8	Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. If excavation in soil cannot be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion, temporary exposed slope surfaces should be covered e.g. by tarpaulin, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place in such a way that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm.	^
S3.4		Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources	^

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		and particularly suited to applications where the influent is pumped.	
S3.4		Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	^
S3.4		Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	^
S3.4		Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.	^
S3.4		Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	NA
S3.4	S5.8	<u>Wheel Washing Water</u> All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	^
S3.4		<u>Drainage</u> It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	^
S3.4		All temporary and permanent drainage pipes and culverts provided	^*

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	
S3.4		All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ.	^
S3.4	S5.8	<u>Sewage Effluent</u> Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the surrounding environment. Regular environmental audit of the construction site will provide an effective control of any malpractices and can encourage continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the project would not cause water pollution problem after undertaking all required measures.	^
S3.4		<u>Stormwater Discharges</u> Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes	^
S3.4		<u>Debris and Litter</u> In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management is optimised	^

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		and that disposal of any solid materials, litter or wastes to marine waters does not occur.	
	S5.8	<u>Boring and Drilling Water</u> Water used in ground boring and drilling for site investigation or rock / soil anchoring should as far as practicable be re-circulated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	^
	S5.8	<u>Acid Cleaning, Etching and Pickling Wastewater</u> Acidic wastewater generated from acid cleaning, etching, pickling and similar activities should be neutralized to within the pH range of 6 to 10 before discharging into foul sewers.	NA
	S5.8	<u>Effluent Discharge</u> There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distance of 100 m should be maintained between the discharge points of construction site effluent and the existing seawater intakes and the planned WSR mentioned in S5.3.1 as appropriate. The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence which is under the ambit of regional office (RO) of EPD.	^
	S5.8	<u>Accidental Spillage</u> Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation, should be observed and complied with for control of chemical wastes. Any service shop and maintenance facilities should be located on	^

Implementation Schedule for Water Quality Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	
	S5.8	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: - Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.	^
	S5.8	- Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.	^
	S5.8	- Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.	^

Implementation Schedule for Waste Management Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.5		<u>Good Site Practices</u> It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are adhered to. Recommendations for good site practices during construction activities include:	
S3.5		- Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	^
	S6.7	- Prepare a Waste Management Plan, which becomes a part of the Environmental Management Plan, in accordance with the requirements stipulated in ETWB TC(W) No. 19/2005, approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites.	^
S3.5	S6.7	- Training of site personnel in proper waste management and chemical waste handling procedures.	^

Implementation Schedule for Waste Management Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.5	S6.7	- Provision of sufficient waste disposal points and regular collection for disposal.	^*
S3.5	S6.7	- Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	^
S3.5		- A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	^
	S6.7	- Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	^
	S6.7	- Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycle.	^
S3.5		<u>Waste Reduction Measures</u> Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:	
S3.5	S6.7	- Sort C&D waste from demolition of the remaining structures to recover recyclable portions such as metals.	NA
S3.5	S6.7	- Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	^
S3.5	S6.7	- Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force.	^
S3.5		- Any unused chemicals or those with remaining functional capacity should be recycled.	^
S3.5	S6.7	- Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	^
S3.5		<u>Construction and Demolition Materials</u> Mitigation measures and good site practices should be incorporated in the contract document to control potential environmental impact from handling and transportation of C&D material. The mitigation measures include:	
S3.5		- Where it is unavoidable to have transient stockpiles of C&D material within the Project work site pending collection for	^

Implementation Schedule for Waste Management Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible.	
S3.5		- Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	^
S3.5		- Skip hoist for material transport should be totally enclosed by impervious sheeting.	^
S3.5		- Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.	^
S3.5		- The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	^
S3.5		- The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.	^
S3.5		- All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.	^
S3.5		- The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.	^
S3.5		- When delivering inert C&D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 “Trip Ticket System for Disposal of Construction and Demolition Materials” should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.	^
	S6.7	- Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation	^

Implementation Schedule for Waste Management Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		of waste.	
S3.5		<u>Chemical Waste</u> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	^
	S6.7	Separation of chemical wastes for special handling and appropriate treatment.	^
S3.5		<u>General Refuse</u> General refuse should be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem.	^

Implementation Schedule for Landscape and Visual Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
S3.8.12		All existing trees should be carefully protected during construction.	^
S3.8.12		Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.	NA
S3.8.12		Control of night-time lighting.	^
S3.8.12		Erection of decorative screen hoarding.	^
	S7.9	<u>Construction Site Control</u> - CM1 - Minimized construction area and contractor's temporary works areas.	^
		- CM2- Control of night-time lighting and glare by hooding all lights.	^
		- CM3 - Erection of decorative mesh screens or construction	^

Implementation Schedule for Landscape and Visual Measures			
EIA for KTD Development Ref.	EIA for KTD – Roads D3A & D4A Ref.	Environmental Protection Measures / Mitigation Measures	Status
		hoardings around works areas in visually unobtrusive colours.	
		- CM4 - Reduction of construction period to practical minimum.	^
		- CM5 - Limitation of / Ensuring no run-off into surrounding landscape and adjacent seawater areas.	^
		- CM6 - Temporary or advance landscape should be provided along the temporary access roads to the Cruise Terminal until such time as road D3 is open.	NA

Remarks:			
^	Compliance of mitigation measure.	X	Non-compliance of mitigation measure.
N/A	Not Applicable at this stage.	●	Non-compliance but rectified by the contractor.
N/A (1)	Not observed.		
*	Recommendation was made during site audit but improved/rectified by the contractor.	#	Recommendation was made during audit and to be improved/ rectified by the contractor.

Mitigation Measures undertaken by the Contractor for site inspections			
			
Date:	04 July 2024	Date:	18 July 2024
Mitigation Measures:	The portable toilets were provided in the construction site.	Mitigation Measures:	The accumulated waste collection was cleared regularly by workers.
			
Date:	18 July 2024	Date:	25 July 2024
Mitigation Measures:	Equipment with NRMM label was used.	Mitigation Measures:	Haul road was sprayed with water to maintain the entire road surface wet.

Appendix Q – Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution

Reporting Month: July 2024

Contract No.	Record of Complaint (Yes/No)	Record of Warning (Yes/No)	Notification of Summons and Successful Prosecutions (Yes/No)
ED/2018/01	No	No	No

Cumulative Statistics on Complaints, Notification of Summons and Successful Prosecutions up to reporting month

Contract No.	Record of Complaint	Record of Warning	Notification of Summons and Successful Prosecutions
ED/2018/01	17	0	0

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
C0001	A dust complaint was referred from the Contractor on 21 Oct 2020 regarding a public complaint via 1823 hotline (Case no. 3-6518939602) on 20 Oct 2020.	1. The water spraying system was not operated in proper time. 2. Stockpile was not covered properly. 3. Haul road was not wetted. 4. Materials transported on trucks were not provided with mechanical covers.	<u>Investigation</u> 1. Based on the information provided by the Contractor on 22 Oct 2020, the water sprinklers system was sprayed every 15 minutes with 70 seconds interval automatically. For the area that water sprinklers system was not covered, manual water spraying was provided. Dump trucks were covered with mechanical cover after loading the materials. The stockpile area was covered by the tarpaulin during night time. 2. Based on the monitoring results on 16 Oct 2020, the 1-hour and 24-hour TSP results were below the Action Levels and Limit Levels. 3. Regular site inspection was conducted by ET on 22 Oct 2020, no adverse observation against the dust impact was recorded. <u>Action taken</u> As per the Contractor, the water sprinkler are now adjusted to start at 8:00am and end at 6:00pm for Monday to Saturday while from 8:00am to 5:00pm on Sunday. Water spraying are set with 5-minute time interval with duration 30-60 seconds. <u>Recommendations</u> To minimize the impact for air quality, mitigation measures should be enhanced specially in dry seasons are recommended: 1. Increase the frequency and duration for automatic water spraying system. 2. Main haul road and the area that water sprinklers system was not covered in the construction site should be wetted by water trucks or manually in regular basis. 3. Ensure stockpiling sites should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting at all time except during working process.	- Closed-out on 5 Nov 2020. - No further complaint was received.
C0002	A dust complaint was referred from the Contractor on 8 Sep 2021 through E-Mail regarding a complaint	Complaint of dust problem at the pavement of Muk Tai Street near Sports	<u>Investigation</u> As per contractor, part of the complaint area was within the site boundary of the project. 1. Manual water spraying was provided. 2. The exposed surface and stockpile areas were covered by the impermeable	- Closed-out on 4 Oct 2021. - No further complaint was received.

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
	received by EPD (EPD ref.: K19/RE/00021205-21) on 7 Sep 2021.	Park.	tarpaulin sheet. <u>Action taken</u> The exposed surface and stockpile area was covered by the impermeable tarpaulin sheet. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however the contractor is recommended to implement the following measures to minimize the impact for air quality: 1. Ensure stockpiling sites should be lined with impermeable sheeting and bundled. 2. Stockpiles should be fully covered by impermeable sheeting at all time except during working process. 3. Ensure the work fulfill the relevant statutory requirements on control of air pollution. 4. Take necessary measures to minimize the environmental nuisance arising from the construction site.	
C0003	A water discharge complaint was referred from the Contractor on 10 Dec 2021 through E-Mail regarding a complaint received by EPD (ref.: K19/RE/00029046-21) on 9 Dec 2021.	Complaint of muddy water being discharged into the sea of To Kwa Wan Typhoon Shelter via a DSD outfall near the roundabout of Shing Fung Road.	<u>Investigation</u> Joint site inspection was conducted by ER, IEC, ET and the contractor on 14 Dec 2021, no adverse observation against the water impact was recorded. 1. There was no muddy water discharge to DSD outfall near the roundabout of Shing Fung Road. 2. The sandbag with layers and filter were provided at the manholes. <u>Action taken</u> - Sandbags and filter were used to block the manholes. - Manholes had been adequately covered and replace the filter frequently. <u>Recommendations</u> There was no direct evidence showing that the water nuisance was caused by the contractor at the complaint area.	- Closed-out on 5 Jan 2022. - No further complaint was received.

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			Some of muddy water generated from wheel washing might be flow to the outfall inside the site boundary, however the contractor had taken the mitigation measure by using sandbag and filter to ease the nuisance. The contractor is recommended to implement the following measures to minimize the impact for waste water: 1. Enhance the sandbag with several layers instead of one layer only and replace the filter frequently. 2. Modify the wheel washing area such that the muddy water will be directly flow to the pit and then waste water treatment facility. 3. Take necessary measures to minimize the environmental nuisance arising from the construction site.	
C0004	A dust complaint was received by EPD on 16 Dec 2022. Contractor received Notification of Environmental Complaints from EPD (ref.: K19/RE/00029136-22) by E-Mail on 22 Dec 2021.	Complaint of mud/ silt being brought out by vehicles from the project site casing mud/silt accumulation on Shing Fung Road.	<u>Investigation</u> Regular site inspection was conducted by ET on 29 Dec 2022. 1. As per the Contractor, mud / slit generated from nearby construction sites might be brought to Shing Fung Road roundabout. 2. No adverse observation against the dust impact was recorded during site inspection. <u>Action taken</u> 1. Watering manually frequently. 2. Haul Road surfaces were wetted by water truck. 3. Wheel washing for the trucks and vehicles before leaving the project site. <u>Recommendations</u> To minimize the impact for air quality, mitigation measures should be enhanced specially in dry seasons are recommended: 1. Increase the frequency and duration for automatic water spraying system. 2. Main haul road and the area that water sprinklers system was not covered in the construction site should be wetted by water trucks or manually in regular basis. 3. Regular wash and clean the share haul road and roundabout in Shing Fung Road.	- Closed-out on 13 Jan 2023. - No further complaint was received.

Complaint Log for ED/2018/01													
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status									
			4. Wheel washing for the trucks and vehicles before leaving the project site. The muddy water after the wheel washing should be directed to sedimentation tank and wastewater treatment facility before discharging to gully. 5. Ensure stockpiling sites should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting at all time except during working process. 6. Dusty materials transported on truck shall be covered.										
C0005	A noise complaint was received by EPD on 21 Dec 2022. Contractor received Notification of Environmental Complaints from EPD (EPD ref.: K19/RE/00029422-22) on 22 Dec 2022. IEC received the notification on 22 Dec 2022 from EPD and forwarded the notification to CEDD, Contractor, ER and ET on same day.	Complaint of construction noise arising from the project site near Shing Kai Road and Muk Tai Street continued to 01:30 am on 21 Dec 2022.	<u>Investigation</u> Regular site inspection was conducted by ET and the Contractor on 29 Dec 2022 1. The complaint was project-related as construction noise arose from the project site near Shing Kai Road and Muk Tai Street. 2. Status of CNPs in the work area near Shing Kai Road and Muk Tai Street were checked and all of them were valid. However, the CNPs only cover the period up to 2300. <table border="1"><thead><tr><th>Construction Noise Permit</th><th>Valid Form</th><th>Valid Till</th></tr></thead><tbody><tr><td>GW-RE1297-22</td><td>10 Dec 2022</td><td>08 Jun 2023</td></tr><tr><td>GW-RE1299-22</td><td>17 Dec 2022</td><td>15 Jun 2023</td></tr></tbody></table> <u>Actions taken</u> 1. Refresher training about CNP was provided to the labour on 22 Dec 2022. 2. No construction activities were allowed in the restricted hours for those areas without valid CNP. <u>Recommendations</u> To minimize the impact of construction noise, the following mitigation measures are recommended: 1. Provide regular training about CNP and other environmental issues to staff. 2. Regularly check the status of ALL CNP and other environmental permits.	Construction Noise Permit	Valid Form	Valid Till	GW-RE1297-22	10 Dec 2022	08 Jun 2023	GW-RE1299-22	17 Dec 2022	15 Jun 2023	- After six months of receiving the complaint, there was no further action from EPD. - Closed-out on 29 Jun 2024.
Construction Noise Permit	Valid Form	Valid Till											
GW-RE1297-22	10 Dec 2022	08 Jun 2023											
GW-RE1299-22	17 Dec 2022	15 Jun 2023											
C0006	A dust complaint was received by EPD on 6	Complaint of construction	<u>Investigation</u> Site inspections were conducted by ET on 26 Jan 2023 and joint site inspection	- Closed-out on 16 Mar 2023.									

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
	Dec 2022. Contractor (POC) received Notification of Environmental Complaints from EPD (ref.: K19/RE/00027862-22) by E-Mail on 7 Dec 2022. IEC received the notification on 19 Jan 2023 and forwarded the notification to CEDD, ER and ET on same day.	dust arising from construction sites along Shing Fung Road.	was conducted by Contractor (POC), ER, ET and IEC on 8 Feb 2023. 1. The concerned area (roundabout) is the common road for public vehicles. In addition, construction vehicles from several nearby construction sites also use the concerned road, especially a lots of dump trucks. 2. Construction vehicles from Contractor (POC) project site are not allowed leaving the site to Shing Fung Road directly as the exit was blocked by barriers since 21 Jan 2023. 3. Worker of sub-contractor from Contractor (POC) wetted the part of the concerned road surface during the site inspection on 8 Feb 2023 to suppress dust emission. 4. No construction works was observed on 26 Jan 2023 and no adverse observation against the dust impact were found during the site inspection on both dates. <u>Action taken</u> 1. Haul Road surfaces were wetted manually and washed the dusty water barrier regularly. 2. Wheel washing for the trucks and vehicles before leaving the project site directly through Shing Fung Road exit. 3. Construction vehicles from Contractor (POC) are not allowed leaving the site to Shing Fung Road directly as the exit was blocked by barriers since 21 Jan 2023. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Main haul road and the area that water sprinklers system was not covered in the construction site should be wetted manually in regular basis. 2. Regular wash the share haul road and roundabout in Shing Fung Road. 3. Wheel washing for the trucks and vehicles before leaving the project site. The muddy water after the wheel washing should be directed to sedimentation tank and wastewater treatment facility before discharging to	

Complaint Log for ED/2018/01				
Complaint Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			gully. 4. Dusty materials transported on truck shall be covered.	
C0007	A dust complaint was received by EPD on 19 Jan 2023. Contractor (POC) received Notification of Environmental Complaints from EPD (ref.: K19/RE/00001988-23) by E-Mail on 2 Feb 2023. IEC received the notification on 2 Feb 2023 and forwarded the notification to CEDD, ER and ET on the same day.	Complaint of dusty environment at the new road connecting Shing Fung Road and Shing Kai Road caused by vehicles from construction sites nearby.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, ET and IEC on 8 Feb 2023. 1. The concerned area (new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 Dec 2022. 2. Construction vehicles from POC are not allowed leaving the site to Shing Fung Road directly with barriers blocked since 21 Jan 2023. 3. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 4. Worker of sub-contractor from Contractor (POC) wetted the part of the concerned road surface during the site inspection on 8 Feb 2023 to suppress dust emission. 5. No adverse observation against the dust impact were found during the site inspection along the new road. <u>Action taken</u> 1. Haul Road surfaces were wetted manually and washed the dusty water barrier regularly. 2. Wheel washing for the trucks and vehicles before leaving the project site. 3. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Main haul road and the area that water sprinklers system was not covered in	- Closed-out on 16 Mar 2023.

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			the construction site should be wetted by water trucks or manually in regular basis. 2. Regular wash the share haul road in Shing Fung Road. 3. Wheel washing for the trucks and vehicles before leaving the project site. The muddy water after the wheel washing should be directed to sedimentation tank and wastewater treatment facility before discharging to gully. 4. Dusty materials transported on truck shall be covered.	
C0008	A dust complaint was received by EPD on 13 Feb 2023. Contractor (POC) received the Notification of Environmental Complaints from EPD (ref.: K19/RE/00003909-23) by E-Mail on 17 Feb 2023 and forwarded the E-mail to ER, ET and IEC on same day.	Complaint of silt / mud accumulation on the new road connecting Shing Fung Road and Shing Kai Road caused by vehicles from construction sites nearby.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, ET and IEC on 23 Feb 2023 and regular site inspection was conducted by Contractor (POC), ER and ET on 2 Mar 2023. 1. The concerned area (new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 Dec 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust nuisance. 2. Construction vehicles from POC are not allowed leaving the site to Shing Fung Road directly with barriers blocked since 21 Jan 2023. 3. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 4. As per Contractor (POC), EPD conducted site visit on 16 Feb 2023. 5. No adverse observation against the dust / muddy water impact were found during the site inspection on both dates. <u>Action taken</u> 1. Construction vehicles from Contractor (POC) are not allowed leaving the site to Shing Fung Road directly as the exit was blocked by barriers since 21 Jan 2023. 2. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023.	- Closed-out on 29 Mar 2023.

Complaint Log for ED/2018/01														
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status										
			3. Haul Road surfaces were wetted manually and washed the dusty water barrier regularly. 4. Wheel washing for the trucks and vehicles before leaving the project site. 5. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted once a week as follow:<table><tr><th>Date</th><th>Road Washing by</th></tr><tr><td>8 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>9 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>14 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>22 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr></table> 6. During the two site inspections, mitigation measures implemented by the Contractor (POC) were found properly based on existing site condition and resources. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Main haul road and the area that water sprinklers system was not covered in the construction site should be wetted by water trucks or manually in regular basis. 2. Regular wash the share haul road in Shing Fung Road. 3. Dusty materials transported on truck shall be covered.	Date	Road Washing by	8 Mar 2023	Sweeper truck with water spraying truck	9 Mar 2023	Sweeper truck with water spraying truck	14 Mar 2023	Sweeper truck with water spraying truck	22 Mar 2023	Sweeper truck with water spraying truck	
Date	Road Washing by													
8 Mar 2023	Sweeper truck with water spraying truck													
9 Mar 2023	Sweeper truck with water spraying truck													
14 Mar 2023	Sweeper truck with water spraying truck													
22 Mar 2023	Sweeper truck with water spraying truck													
C0009	A dust complaint was received by EPD on 15 Feb 2023. Contractor (POC) received the Notification of Environmental	Complaint of mud / silt being brought out by vehicles from construction site at Shing Fung Road roundabout	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, ET and IEC on 23 Feb 2023 and regular site inspection was conducted by Contractor (POC), ER and ET on 2 Mar 2023. 1. The concerned area (new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 Dec 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust nuisance.	- Closed-out on 29 Mar 2023.										

Complaint Log for ED/2018/01														
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status										
	Complaints from EPD (ref.: K19/RE/00004280-23) by E-Mail on 22 Feb 2023 and forwarded the E-mail to ER, ET and IEC on same day.	(near Lamp Post DF4831) causing mud / silt accumulation along Shing Fung Road.	2. Construction vehicles from POC are not allowed leaving the site to Shing Fung Road directly with barriers blocked since 21 Jan 2023. 3. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 4. As per Contractor (POC), EPD conducted site visit on 16 Feb 2023. 5. No adverse observation against the dust impact were found during the site inspection on both dates. Action taken 1. Construction vehicles from Contractor (POC) are not allowed leaving the site to Shing Fung Road directly as the exit was blocked by barriers since 21 Jan 2023. 2. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 3. Haul Road surfaces were wetted manually and washed the dusty water barrier regularly. 4. Wheel washing for the trucks and vehicles before leaving the project site. 5. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted once a week as follow: <table><tr><th>Date</th><th>Road Washing by</th></tr><tr><td>8 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>9 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>14 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>22 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr></table> 6. During the two site inspections, mitigation measures implemented by the Contractor (POC) were found properly based on existing site condition and resources. Recommendations There was no direct evidence showing that the dust nuisance was caused by the	Date	Road Washing by	8 Mar 2023	Sweeper truck with water spraying truck	9 Mar 2023	Sweeper truck with water spraying truck	14 Mar 2023	Sweeper truck with water spraying truck	22 Mar 2023	Sweeper truck with water spraying truck	
Date	Road Washing by													
8 Mar 2023	Sweeper truck with water spraying truck													
9 Mar 2023	Sweeper truck with water spraying truck													
14 Mar 2023	Sweeper truck with water spraying truck													
22 Mar 2023	Sweeper truck with water spraying truck													

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Main haul road and the area that water sprinklers system was not covered in the construction site should be wetted by water trucks or manually in regular basis. 2. Regular wash the share haul road in Shing Fung Road. 3. Dusty materials transported on truck shall be covered.	
C0010	A dust and muddy water complaint was received by Hotline 1823 on 9 Mar 2023. ER received the transfer from the Hotline 1823 on 9 Mar 2023 and forwarded the E-mail to Contractor (POC), ET and IEC on same day.	Complaint of dusty environment at the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road roundabout. Worker wetted the road surface and might cause mud / silt problem.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, and ET on 16 Mar 2023 and 23 Mar 2023. 1. The concerned area (new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 Dec 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust nuisance. 2. Construction vehicles from POC are not allowed leaving the site to Shing Fung Road directly with barriers blocked since 21 Jan 2023. 3. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 4. The sandbags were provided around the manholes. 5. No adverse observation against the dust / muddy water impact were found during the site inspection on both dates. <u>Action taken</u> 1. Construction vehicles from Contractor (POC) are not allowed leaving the site to Shing Fung Road directly as the exit was blocked by barriers since 21 Jan 2023. 2. Contractor (POC) has restricted the construction vehicles from nearby construction site (Gammon site) using this site entrance for any construction activities since 4 Feb 2023. 3. Haul Road surfaces were wetted manually and washed the dusty water barrier regularly. 4. Wheel washing for the trucks and vehicles before leaving the project site.	- Closed-out on 6 Apr 2023.

Complaint Log for ED/2018/01														
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status										
			5. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted once a week as follow:<table><tr><th>Date</th><th>Road Washing by</th></tr><tr><td>8 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>9 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>14 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>22 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr></table> 6. The sandbags were provided around the manholes. 7. During the two site inspections, mitigation measures implemented by the Contractor (POC) were found properly based on existing site condition and resources. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air and water quality: 1. Dusty materials transported on truck shall be covered. 2. Enhance the sandbags with several layers of filters and replace the filter frequently.	Date	Road Washing by	8 Mar 2023	Sweeper truck with water spraying truck	9 Mar 2023	Sweeper truck with water spraying truck	14 Mar 2023	Sweeper truck with water spraying truck	22 Mar 2023	Sweeper truck with water spraying truck	
Date	Road Washing by													
8 Mar 2023	Sweeper truck with water spraying truck													
9 Mar 2023	Sweeper truck with water spraying truck													
14 Mar 2023	Sweeper truck with water spraying truck													
22 Mar 2023	Sweeper truck with water spraying truck													
C0011	A muddy water complaint was received by EPD on 9 Mar 2023. Contractor (POC) received the Notification of Environmental Complaints from EPD (ref.: K19/RE/00004280-23)	Complaint of water being sprayed onto vehicles passing by and mud / silt being washed into roadside gully near Shing Fung Road roundabout.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER and ET on 23 Mar 2023. 1. The concerned area (new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 Dec 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust / mud / silt nuisance. 2. The sandbags were provided around the manholes. 3. No adverse observation against the muddy water impact were found during the site inspection on both dates.	- Closed-out on 6 Apr 2023.										

Complaint Log for ED/2018/01														
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status										
	by E-Mail on 22 Feb 2023 and forwarded the E-mail to ER, ET and IEC on same day.		<u>Action taken</u> 1. As per Contractor (POC), no manually road surfaces watering on Shing Fung Road after receiving complaint (16 Mar 2023). 2. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted once a week as follow: <table><tr><th>Date</th><th>Road Washing by</th></tr><tr><td>8 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>9 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>14 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>22 Mar 2023</td><td>Sweeper truck with water spraying truck</td></tr></table> 3. The sandbags were provided around the manholes. <u>Recommendations</u> There was no direct evidence showing that the muddy water nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air and water quality: 1. Enhance the sandbags with several layers of filters and replace the filter frequently.	Date	Road Washing by	8 Mar 2023	Sweeper truck with water spraying truck	9 Mar 2023	Sweeper truck with water spraying truck	14 Mar 2023	Sweeper truck with water spraying truck	22 Mar 2023	Sweeper truck with water spraying truck	
Date	Road Washing by													
8 Mar 2023	Sweeper truck with water spraying truck													
9 Mar 2023	Sweeper truck with water spraying truck													
14 Mar 2023	Sweeper truck with water spraying truck													
22 Mar 2023	Sweeper truck with water spraying truck													
C0012	A dust complaint was received by EPD on 31 May 2023.	Complaint of silt / mud accumulation on the new road connecting Shing Fung Road and Shing Kai Road caused by vehicles from construction site nearby.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER and ET on 8 June 2023. 1. As per Mr. Tony Tang from POC, the concerned area was the section of Shing Fung Road at the entrance of Gammon site accommodation. 2. The new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 December 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust / silt nuisance. 3. As per Mr. Tony Tang from POC, recycled water was used in wheel washing machine near the entrance of Gammon site. Those are the possible sources of mud nuisance.	- Closed-out on 19 June 2023.										

Complaint Log for ED/2018/01																						
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status																		
	2023 and forwarded the E-mail to ER, ET and IEC on same day.		4. No adverse observation against the dust impact were found during the site inspection. <u>Action taken</u> 1. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted twice a week start from 11 May 2023. <table><tr><th>Date</th><th>Road Washing by</th></tr><tr><td>19 May 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>23 May 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>25 May 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>30 May 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>2 June 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>6 June 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>9 June 2023</td><td>Sweeper truck with water spraying truck</td></tr><tr><td>13 June 2023</td><td>Sweeper truck with water spraying truck</td></tr></table> 2. Wheel washing for the vehicles before leaving the construction site. <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Regular wash the share haul road in Shing Fung Road and Shing Kai Road. 2. Dusty materials transported on truck should be covered.	Date	Road Washing by	19 May 2023	Sweeper truck with water spraying truck	23 May 2023	Sweeper truck with water spraying truck	25 May 2023	Sweeper truck with water spraying truck	30 May 2023	Sweeper truck with water spraying truck	2 June 2023	Sweeper truck with water spraying truck	6 June 2023	Sweeper truck with water spraying truck	9 June 2023	Sweeper truck with water spraying truck	13 June 2023	Sweeper truck with water spraying truck	
Date	Road Washing by																					
19 May 2023	Sweeper truck with water spraying truck																					
23 May 2023	Sweeper truck with water spraying truck																					
25 May 2023	Sweeper truck with water spraying truck																					
30 May 2023	Sweeper truck with water spraying truck																					
2 June 2023	Sweeper truck with water spraying truck																					
6 June 2023	Sweeper truck with water spraying truck																					
9 June 2023	Sweeper truck with water spraying truck																					
13 June 2023	Sweeper truck with water spraying truck																					
C0013	A water complaint was received by EPD on 19 June 2023.	- Complaint of muddy water being discharged into Kai Tak Approach Channel on 18 Jun	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER and ET on 6 Jul 2023. 1. As per Mr. Tony Tang from POC, the concerned area was the section of Shing Fung Road at the nearby channel. 2. Heavy raining was recorded on 18 Jun 2023. The recorded rainfall was 35.8mm (sourced from manned weather station of Hong Kong Observatory at https://www.hko.gov.hk/en/cis/dailyExtract.htm?y=2023&m=6). The	- Closed-out on 2 Aug 2023.																		

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
	Complaints from EPD (ref.: K19/RE/00014944-23) by E-Mail on 29 June 2023 and forwarded the E-mail to ER, ET and IEC on 4 July 2023.	2023. - Complaint of construction work being conducted on the Sunday of 18 Jun 2023.	implication of heavy rainfall storm runoff might wash across the exposed soil surfaces which was direct muddy water discharge. This is the possible source of water nuisance. 3. As per Mr. Tony Tang from POC, no construction work was conducted on 18 Jun 2023. Based on the attendance record, 6 employees including 4 watchman, labourer and driver, were on site on 18 Jun 2023 and they were not involved in the construction work. In the joint site inspection, no construction work was conducted on the nearby channel. 4. No adverse observation against the muddy water impact were found during the site inspection on 14 and 20 June 2023, and 6 July 2023. The sedimentation tank and wastewater treatment plant are operating efficiently during the site inspection. <u>Action taken</u> 1. The ditch is maintained regularly and excavated deeper by workers. 2. Pumps are placed at the ditch to prevent flooding and overflow. 3. Enhanced training for site workers to prevent flushing during heavy rain by placing pumps in the ditch to prevent flooding and overflow during periods of heavy rain during Tool- Box-Talk training. <u>Recommendations</u> There was no direct evidence showing that the muddy water nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for water quality: 1. Regular cleaning and maintenance drainage systems at the nearby Kai Tak Approach Channel.	

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
C0014	A polluting discharge complaint was received by EPD on 16 October 2023. Contractor (POC) received the Notification of Environmental Complaints from EPD (ref.: K19/RE/00024581-23) by E-Mail on 19 October 2023 and forwarded the E-mail to ER, ET and IEC on 21 October 2023.	- Complaint of polluting discharge from the construction site of Stage 4 Infrastructure at the Former Runway and South Apron, Kowloon City (“illegal discharge from kai tak 6577 construction site the main contractor should be hip hing)	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER and ET on 26 October 2023. 1. The concerned area is near at Former Runway and South Apron, Kowloon City. Those are the possible sources should be illegal discharge from Kai Tak 6577 construction site which the main contractor should be hip hing. The possible source of polluting discharge does not come from the Contractor (POC). 2. No adverse observation against the muddy water impact were found during the site inspection on dates. No surface runoff is observed, and the sedimentation tank and wastewater treatment plant were implemented normally. <u>Action taken</u> 1. As per Contractor (POC), no wastewater generated at concerned area and ensure fulfil the conditions stipulated in the valid WPCO licence after receiving complaint (16 October 2023). The effluent discharge has been implemented properly. 2. The silt curtain has been installed around the construction activities at the concerned area. (referring to Photo 2) The sedimentation tank and wastewater treatment has been implemented properly. 3. The pump has been installed and collected sewage at the channel which can minimize water quality impacts and prevent overload the foul sewage system. (referring to Photo 3) The channel and ditches have been clear after receiving complaint. <u>Recommendations</u> There was no direct evidence showing that the muddy water nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for water quality:	- Closed-out on 15 November 2023.

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			1. The silt removal facilities, channels and manholes should be maintained regularly. 2. The silt curtain and equipment should be properly maintained.	

Complaint Log for ED/2018/01					
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations		Close-Out Date / Status
C0015	A dust complaint was received by EPD on 12 December 2023. Contractor (POC) received the Notification of Environmental Complaints from EPD (ref.: K19/RE/00030287-23) by E-Mail on 19 December 2023 and forwarded the E-mail to ER, ET and IEC on 20 December 2023.	- Complaint of construction dust nuisance on Shing Fung Road.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, and ET on 21 December 2023. 1. As per the email clarified by Mr. Tony Tang from POC on 20 December 2023, the concerned area (section of Shing Fung Road) was the junction of Road D3 and gate 2A& 2B. 2. The new road connecting Shing Fung Road & Shing Kai Road) has been open for public vehicles (not only project related vehicles) since 31 December 2022. Vehicles from nearby construction sites also used the concerned road. Those are the possible sources of dust / silt nuisance. The non-project of stockpiles is founded near the concerned road during the site inspection. 3. 3. As per Mr. Tony Tang from POC, recycled water was used in wheel washing machine near the entrance of Gammon site. The washing facilities and regular road watering are implemented. 4. No adverse observation against the dust impact were found during the site inspection. The washing facilities and dust control measures are implemented properly. <u>Action taken</u> 1. As per instruction from CEDD and AECOM, road washing along the new road (connecting Shing Fung Road and Shing Kai Road) and Shing Fung Road by water truck was conducted once per week in December 2023.		- 17 January 2024
			Date	Road Washing by	

Complaint Log for ED/2018/01					
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations		Close-Out Date / Status
			07 December 2023	Sweeper truck with water spraying truck	
			16 December 2023	Sweeper truck with water spraying truck	
			21 December 2023	Sweeper truck with water spraying truck	
			29 December 2023	Sweeper truck with water spraying truck	
			2. Wheel washing for the vehicles before leaving the construction site.		
<u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality: 1. Regular wash the share haul road in Shing Fung Road and Shing Kai Road. 2. Dusty materials transported on truck should be covered.					

Complaint Log for ED/2018/01																													
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations					Close-Out Date / Status																					
C0016	A dust complaint was received by Hotline 1823 on 20 May 2024. ER (AECOM) and Contractor (POC) received the transferred from Hotline 1823 (Case No. 3-8226038234) on 20 May 2024 and forwarded the E-mail to ET, and IEC on same day.	- The dust emission generated from a excavator near EVA No. 10 which affecting the surroundin g residents. The complaina nt also expressed doubt the effectivene ss of implement ation of environme ntal manageme nt system.	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, and ET on 23 May 2024. 1. The complaint is not directly project-related since C&D stockpiling works from nearby construction sites. (locations referring to Attachment 2) Those are the possible sources of dust nuisance. 2. As per the email reply by Mr. Tony Tang from POC on 21 May 2024, the concerned area (section of Shing Fung Road) was near EVA No. 10. The POC proposed to implement measures for mitigate the dust nuisance. 3. The nearest surrounding resident to the concerned area is 580.23m (locations referring to Attachment 1) 4. As per Mr. Tony Tang from POC, POC will provide a worker starting from 22 May 2024 to spray water at the concerned location (Near EVA No. 10) within office hour to suppress dust emission no matter there is any loading or unloading of dusty materials site activities. (locations referring to Attachment 3) 5. Based on the monitoring results on 20 May 2024, 1-hour and 24-hour TSP results were below the Action Levels and Limit as shown as below. <table><tr><td></td><td colspan="2">AM3</td><td colspan="2">AM4(A)</td><td colspan="2">AM7</td></tr><tr><td></td><td>1-hour TSP</td><td>24-hour TSP</td><td>1-hour TSP</td><td>24-hour TSP</td><td>1-hour TSP</td><td>24-hour TSP</td></tr><tr><td>Measured result (µg/m³)</td><td>44 -48</td><td>42</td><td>56-63</td><td>/</td><td>53 – 57</td><td>54</td></tr></table>						AM3		AM4(A)		AM7			1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP	Measured result (µg/m³)	44 -48	42	56-63	/	53 – 57	54	- Closed-out on 04 June 2024
	AM3		AM4(A)		AM7																								
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP																							
Measured result (µg/m³)	44 -48	42	56-63	/	53 – 57	54																							

Complaint Log for ED/2018/01										
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations							Close-Out Date / Status
			Action Level (µg/m³)	297	182	326	187	315	181	
			Limit Level (µg/m³)	500	260	500	260	500	260	
			6. The effectiveness of the environmental management system implemented has been reviewed. 7. No adverse observation against the dust impact were found during the site inspection. The dust control measures are implemented properly. (referring to Attachment 4) <u>Action taken</u> 1. Regularly monitor all the Powered Mechanical Equipment (PME) to ensure no dark smoke emission. (refer to Attachment 3). 2. Arrange to cover the stockpile with tarpaulin sheet to prevent dust emission. (refer to Attachment 3) 3. Arrange resources to spray water during excavator loading and unloading of dusty material which have including fill material and sub-base. (refer to Attachment 3) <u>Recommendations</u> There was no direct evidence showing that the dust nuisance was caused by the contractor at the complaint area, however Contractor (POC) is recommended to implement the following measures to minimize the impact for air quality:							

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			1. The share haul road in Shing Fung Road should be washed regularly. 2. Dust mitigation control should be done at the work site 8 times per day. 3. Stockpiling sites should be lined with impermeable sheeting and bunded. 4. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.	

Complaint Log for ED/2018/01				
Complaint Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
C0017	A waste management complaint was received by Hotline 1823 on 25 May 2024. The public complaint is received via 1823 (Case No.: 3-8234938050) on 25 May 2024 and forwarded by CEDD on 27 May 2024, and forwarded to ER, Contractor, ET and IEC.	- Rodent problem at the junction of Shing Kai Road & Shing Fung Road	<u>Investigation</u> Joint site inspection was conducted by Contractor (POC), ER, IEC and ET on 30 May 2024. 1. Accumulation of waste was found in the concerned area, the grade road (Shing Kai Road to NSR) and the junction of Road D3 (Shing Kai Road Junction). (refer to Photo Record 7 of Attachment 3) 2. No trace of rats was found during inspection but flies were present. (refer to Photo Record 6 of Attachment 3) 3. Waste management measures were not implemented properly. There were no sufficient waste disposal points and regular dispose of waste at the concerned area (refer to Photo Record 8 of Attachment 3). 4. The complaint was project-related as improper disposal of waste could lead to occurrence of rats. <u>Action taken</u> 1. Poisonous rat bait was placed within the site boundary (refer to Photo Record 2,3,4 of Attachment 3). 2. Workers received regular briefing about proper waste management (refer to Photo Record 5 of Attachment 3). 3. The general waste was collected and removed after site inspection on 30 May 2024. (refer to Photo Record 9 and 10 of Attachment 3). <u>Recommendations</u> There was related evidence showing that the waste nuisance at the concerned area was caused by the Contractor (POC). However, it is recommended to	- Closed-out on 04 June 2024

Complaint Log for ED/2018/01				
Complain t Ref. No.	Date of Complaint	Description of Complaint	Investigation / Actions taken / Recommendations	Close-Out Date / Status
			implement the following measures to minimize the impact of waste accumulation 1. Multiple waste disposal points should be set up for proper waste storage. 2. Frequency of waste cleaning and collection should be increased to prevent waste accumulation. 3. Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycle.	
