

Date: 14 March 2025
Your ref:
Our ref: PL-202503045

AECOM Asia Company Limited
12/F, Grand Central Plaza, Tower 2,
138 Shatin Rural Committee Road,
Shatin, New Territories,
Hong Kong

Attn.: Ms. Mavis Law, SRE

Dear Ms. Law,

Agreement No. EDO 6/2019
Independent Environmental Checker for Contract No. ED/2018/05 Kai Tak Development –
Stage 5B Infrastructure Works at the Former North Apron Area
Verification of Monthly EM&A Report (February 2025)

Reference is made to the Monthly EM&A Report (February 2025) (Version 1.2) issued by the Environmental Team on 14 March 2025.

Please be informed that we have no adverse comment on the captioned submission. We hereby verify the Monthly EM&A Report (February 2025) in accordance with Condition 3.3 of Environmental Permit No. EP-337/2009.

Thank you for your attention.

Yours sincerely,
For and on behalf of
Acuity Sustainability Consulting Limited



Kevin Li
Independent Environmental Checker


c.c.	CEDD	Attn.: Mr. Michael So	By email
	Ka Shing	Attn.: Mr. Chan Pang (ETL)	By email

Environmental Monitoring and Audit Report
for
Contract No. ED/2018/05 –
Kai Tak Development – Stage 5B infrastructure
works at the former north apron area

Contract No.: EDO 2/2020

February 2025

(Version 1.2)

Certified By:  _____

(Environmental Team Leader)

Table of Content	Page
EXECUTIVE SUMMARY	5
Breaches of Action and Limit Levels.....	5
Complaint log	5
Notifications of summons and successful prosecutions	6
Report changes.....	6
Key construction works in the reporting month	6
Future key issues.....	7
1. INTRODUCTION.....	8
Project Background.....	8
Project Organization.....	9
Works Area and Construction Programme.....	9
Construction works undertaken during reporting month	10
Submission Status under the Environmental Permits	10
2. AIR QUALITY MONITORING.....	11
Monitoring Requirements.....	11
Monitoring Locations.....	11
Monitoring Parameters, Frequency and Duration.....	11
Monitoring Equipment	12
Monitoring Methodology and QA/QC Procedure	13
Wind Data Monitoring	15
Action and Limit Levels.....	15
Impact Air Quality Monitoring results.....	16
3. NOISE MONITORING.....	17
Monitoring Requirements.....	17
Monitoring Locations.....	17

	Monitoring Parameters, Frequency and Duration.....	17
	Monitoring Equipment.....	18
	Monitoring Methodology and QA/QC Procedure	18
	Maintenance and Calibration.....	19
	Action and Limit Levels.....	19
	Impact Noise Monitoring results	20
4.	COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS	21
5.	LANDSCAPE AND VISUAL MONITORING	23
	Results and Observations	23
6.	ENVIRONMENTAL SITE INSPECTION AND AUDIT	24
	Site Inspection	24
	Status of Waste Management	25
	Status of Environmental Licenses, Notification and Permits.....	25
	Implementation Status of Environmental Mitigation Measures.....	26
	Environmental Complaint and Non-compliance	26
	Notifications of summons and successful prosecutions.....	27
7.	FUTURE KEY ISSUES	28
	Construction Programme in the coming month.....	28
	Environmental Site Inspection and Monitoring Schedule for next month.....	29
8.	CONCLUSIONS	30

List of Tables

Table I	Non-compliance Record in the Reporting Month
Table II	Summary of complaints in the Reporting Month
Table III	Summary of summons and successful prosecutions in the Reporting Month
Table IV	Summary of future key issues and potential impact in the coming month
Table 1.1	Contact Information of Key Personnel

Table 1.2	Major activities of the Project during reporting month
Table 1.3	Summary of Status of Required Submission of EPs
Table 2.1	Locations of Air Quality Monitoring Stations
Table 2.2	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.3	Air Quality Monitoring Equipment
Table 2.4	Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring
Table 2.5	Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring
Table 2.6	Summary of 24-hour average TSP Monitoring Data during the reporting month
Table 2.7	Summary of 1-hour average TSP Monitoring Data during the reporting month
Table 3.1	Locations of Noise Monitoring Stations
Table 3.2	Noise Monitoring Parameters, Frequency and Duration
Table 3.3	Noise Monitoring Equipment
Table 3.4	Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring
Table 3.5	Summary of Noise Monitoring Data during the reporting month
Table 4.1	Comparison of 24-hour average TSP Monitoring Data with EIA predictions
Table 4.2	Comparison of 1-hour average TSP Monitoring Data with EIA predictions
Table 4.3	Comparison of Noise Monitoring Data with EIA predictions
Table 5.1	Summary of observations of Landscape and Visual impact during the reporting month
Table 6.1	Summary of site inspections observations during the reporting month
Table 6.2	Summary of Environmental Licenses, Notifications and Permits
Table 6.3	Summary of complaints in the Reporting Month
Table 6.4	Summary of summons and successful prosecutions in the Reporting Month
Table 7.1	Summary of future key issues and potential impact in the coming month

List of Figure

Figure 1 – Proposed works of Contract No. ED/2018/05

Figure 2 – Proposed works of Contract No. ED/2018/05

Figure 3 – D1 Road Site Layout Plan

Figure 4 – Site Layout Plan

Figure 5 – Air Quality Monitoring Stations

Figure 6 – Noise Monitoring Stations

List of Appendices

Appendix A – Organization Chart of EM&A Team

Appendix B – Construction Programme

Appendix C – Environmental monitoring schedules

Appendix D – Photographic records

Appendix E – Calibration certificates, catalogue of air quality monitoring equipment

Appendix F – Weather information

Appendix G – 24-hr TSP monitoring results and graphical presentation

Appendix H – 1-hr TSP monitoring results and graphical presentation

Appendix I – Event and Action Plan for air quality

Appendix J – Calibration certificates, catalogue of noise monitoring equipment

Appendix K – Noise monitoring results and graphical presentation

Appendix L – Event and Action Plan for noise

Appendix M – Event and Action Plan for Landscape and Visual Impact

Appendix N – Waste Flow Table

Appendix O – Environmental Mitigation Implementation Schedule (EMIS)

Appendix P – Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution

EXECUTIVE SUMMARY

1. This is the 49th Monthly Environmental Monitoring & Audit (EM&A) report which summarises the findings of the EM&A Programme during the reporting period from 1 to 28 February 2025.

Breaches of Action and Limit Levels

2. 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
3. 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
4. Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
5. Summary of the non-compliance in the reporting month for the Project is tabulated in Table I.

Table I Non-compliance Record in the Reporting Month

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
1-hr TSP	0	0	N/A
24-hr TSP	0	0	N/A
Construction noise	0	0	N/A

Complaint log

6. No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table II.

Table II Summary of complaints in the Reporting Month

Date of complaint received	Date of complaint	Description of complaint	Recommendations / Action taken	Close-out date / Status
No complaint was received in the reporting month.	NA	NA	NA	NA

Notifications of summons and successful prosecutions

7. No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table III.

Table III Summary of summons and successful prosecutions in the Reporting Month

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
No notification of summons and successful prosecutions were received in the reporting month.	NA	NA	NA	NA

Report changes

8. There was no reporting change in the reporting month.

Key construction works in the reporting month

9. Major construction activities undertake during the reporting month included:

- Installation of cable tray at LW-02
- Installation of lighting system at LW-02
- Tiling works at LW-02
- Lift installation at LW-02
- Installation of canopy at LW-02
- Installation of glass panel and aluminum panels at LW-02
- Installation of glass balustrade at bridge deck of LW02
- Installation of geotextile and subsoil drainage for planters at LW02

- Construction of parapet for S14
- Refurbishment for Bridge K73
- Asphalt application at S14
- Drainage construction of S14
- Installation of movement joint for S14
- Construction of headwall at Subway SB-01 Retrieval Shaft
- Ceiling painting and plastering inside Subway SB-01
- Road and drain construction works for Road L16, Road L9 and Road D1
- Construction works for DCS
- Watermain and road works at PS3

10. The future key issues and potential impact in the coming month are given in Table IV.

Table IV Summary of future key issues and potential impact in the coming month

Future key issues in the coming month	Potential impact
Installation of E&M equipment for pillar box at LW-02	Noise and Air Quality
Lift installation at LW-02	Noise and Air Quality
Installation of glass panels and aluminum panels of LW-02	Noise and Air Quality
Installation of glass balustrade at LW02	Noise and Air Quality
Planting works at LW02	Noise and Air Quality
Tiling works at LW02	Noise and Air Quality
Construction of Parapet for S14	Noise and Air Quality
Refurbishment works for Bridge K73	Noise and Air Quality
Construction of bridge deck of S14	Noise and Air Quality
Drainage construction works at PS2	Noise and Air Quality
Construction of end wall at Subway SB-01 Retrieval Shaft	Noise and Air Quality
Finishing works of Subway SB-01	Noise and Air Quality
Construction of top slab of lift tower at Subway SB-01	Noise and Air Quality
Demolition of accessible ramp inside SB01	Noise and Air Quality
Excavation works for construction of staircase at Subway SB-01	Noise and Air Quality
Tiling works for Subway SB-01	Noise and Air Quality
Road and drain construction works for Road L16, Road L9 and Road D1 and	Noise and Air Quality
Construction works for DCS	Noise and Air Quality

1. INTRODUCTION

Project Background

- 1.1 The Kai Tak Development (KTD) is located in the southern part of Kowloon Peninsula of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling.
- 1.2 Contract No. ED/2018/05 - Kai Tak Development – stage 5B infrastructure works at the former north apron area (The Project), comprises mainly the design and construction of a section of dual two-lane Road D1; single two-lane Road L9 and Road L16; a single-lane slip road S14; a pedestrian subway SB-01; an elevated walkway LW-02; renovation of the existing pedestrian subways KS9, KS10 and KS32, as well as modification of the southern end of the existing pedestrian subway KS10; associated footpaths, street lighting, traffic aids, drainage, sewerage, water mains, landscaping, electrical and mechanical works, and ancillary works. The proposed works are shown in Figure 1 and Figure 2. The proposed works and site boundary are shown in Figure 3 and Figure 4. Civil Engineering and Development Department (CEDD) had completed an Environmental Impact Assessment (EIA) and is the Permit Holder.
- 1.3 In accordance with the approved EIA Reports, Environmental Monitoring and Audit (EM&A) programmes are recommended to ensure compliance with the EIA study recommendations. The project proponent was the Civil Engineering and Development Department (CEDD). AECOM Asia Co. Ltd. (AECOM) was commissioned by CEDD as Supervisor (act as Engineers' Representative (ER) listed in EM&A Manual). Acuity Sustainability Consulting Limited (Acuity) was commissioned as the Independent Environmental Checker (IEC). Build King – STEC Joint Venture (Build King) was appointed as the main Contractor for the construction works of Contract No. ED/2018/05. Ka Shing was commissioned by CEDD to undertake the role of the Environmental Team (ET) to implement the EM&A programme for The Project.
- 1.4 The construction work under ED/2018/05 comprises the EM&A Manual (EIA Register No. AEIAR-130/2009 for Kai Tak Development) and Environmental Permit No. EP- 337/2009.
- 1.5 Air quality and noise monitoring has been proposed in the EM&A Manual with EIA Register No. AEIAR-130/2009 for Kai Tak Development.

Project Organization

1.6 The project organization chart and with respect to the EM&A programme is shown in Appendix A. Information of key personnel contact names and telephone numbers are summarized in Table 1.1.

Table 1.1 Contact Information of Key Personnel

Party	Role	Contact Person	Position	Phone No.	E-mail
Civil Engineering and Development Department (CEDD)	Project Proponent	Mr. Stephen Lo	Permit Holder	3579 2470	cclo@cedd.gov.hk
AECOM Asia Co. Ltd. (AECOM)	Supervisor (act as Engineers' Representative (ER) listed in EM&A Manual)	Mr. Vincent Lee	Supervisor's Delegate	2798 0771	sre2@ktd-stage5.com
Acuity Sustainability Consulting Limited (Acuity)	Independent Environmental Checker (IEC)	Mr. Kevin Li	IEC	9779 2247	kevin.li@aurecongroup.com
Ka Shing Management Consultant Limited (Ka Shing)	Environmental Team (ET)	Mr. Pang Chan	ET Leader	6082 2973	stage5b@ka-shing.net
Build King – STEC Joint Venture (BK-STECC)	Contractor	Mr. Rex Lau	Contractor's Representative	6282 5154	rex.lau@buildking.hk

Works Area and Construction Programme

1.7 The construction works commenced on 16 February 2021. The construction programme of the Project is given in Appendix B.

Construction works undertaken during reporting month

1.8 Major construction works of the Project in the reporting month are summarized in Table 1.2:

Table 1.2 Major activities of the Project during reporting month

Installation of cable tray at LW-02	Installation of movement joint for S14
Installation of lighting system at LW-02	Construction of headwall at Subway SB-01 Retrieval Shaft
Tiling works at LW-02	Ceiling painting and plastering inside Subway SB-01
Lift installation at LW-02	Road and drain construction works for Road L16, Road L9 and Road D1
Installation of canopy at LW-02	Construction works for DCS
Installation of glass panel and aluminum panels at LW-02	Watermain and road works at PS3
Installation of glass balustrade at bridge deck of LW02	
Installation of geotextile and subsoil drainage for planters at LW02	
Construction of parapet for S14	
Refurbishment for Bridge K73	
Asphalt application at S14	
Drainage construction of S14	

Submission Status under the Environmental Permits

1.9 The status of required submission under Environmental Permit (EP) conditions under EP-337/2009 are summarized in Table 1.3.

Table 1.3 Summary of Status of Required Submission of EPs

EP Condition EP-337/2009	Submission	Submission Date
Condition 1.11	Notification of Commencement Date of Construction of the Project	12 Jan 2021
Condition 2.3	Management Organization of Main Construction Companies	21 Sep 2020
Condition 2.3	Updated Management Organization of Main Construction	4 July 2022

EP Condition EP-337/2009	Submission	Submission Date
	Companies	
Condition 2.4	Design Drawings	12 Jan 2021
Condition 2.11	Landscape Mitigation Plans	17 Dec 2020
Condition 3.2	Baseline Monitoring Report	12 Jan 2021
Condition 3.3	Monthly EM&A Report (Jan 2025)	14 Feb 2025

2. AIR QUALITY MONITORING

Monitoring Requirements

2.1 In accordance with EM&A Manual (EIA Register No. AEIAR-130/2009), impact air quality monitoring shall be carried out during the construction phase of the Project. For regular impact monitoring, a sampling frequency of at least once in every six days will be strictly observed at all of the monitoring stations for 24-hour TSP. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days will be undertaken when the highest dust impact occurs.

Monitoring Locations

2.2 Two designated monitoring stations were selected for air quality monitoring programme. Impact air quality monitoring was conducted at two air quality monitoring stations in the reporting month. Table 2.1 describes the air quality monitoring locations, which are also depicted in Figure 5.

Table 2.1 Locations of Air Quality Monitoring Stations

Air Quality Monitoring Locations for the Project	Location of Measurement
AM2(A) – Ng Wah Catholic Secondary School	Rooftop
AM3 – Sky Tower	Podium floor near T7

Monitoring Parameters, Frequency and Duration

2.3 The air quality monitoring locations and monitoring frequency are listed in Table 2.2.

Table 2.2 Air Quality Monitoring Parameters, Frequency and Duration

Air Monitoring Station	Location for Measurement	Parameter	Duration	Frequency
AM2(A) – Ng Wah Catholic Secondary School	Rooftop	- 24-hour average TSP	- 24 hours	- Once every 6 days
AM3 – Sky Tower	Podium Floor near Tower 7	- 1-hour average TSP	- 1 hour	- Three times every 6 days

2.4 The monitoring schedule for reporting month and next month is presented in Appendix C.

2.5 Photographic records of the impact monitoring setup are shown in Appendix D.

Monitoring Equipment

2.6 24-hour average TSP and 1-hour average TSP levels were measured for impact monitoring. 24-hour average TSP levels were measured by the High Volume Samplers (HVS) and 1-hour average TSP levels were measured by direct reading method to indicate short-term impacts. Wind data monitoring equipment was set up at conspicuous locations for logging wind speed and wind direction near to the dust monitoring locations. Table 2.3 summarizes the equipment to be used in the air quality monitoring.

Table 2.3 Air Quality Monitoring Equipment

Equipment	Model	Quantity	Calibration Interval
HVS Sampler	TE-5170 X c/w of TSP sampling inlet	2	2 months
HVS Calibrator	TISCH TE-5025A	1	1 year
1-hour TSP Dust Meter	TSI Model AM510 SidePak Personal Aerosol Monitor	2	1 year
Weather Station	Davis Vantage Pro2 Weather Station	1	6 months

2.7 High volume samplers (HVS) (TE-5170 X c/w of TSP sampling inlet) comprising with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

2.8 Calibration certificates, catalogue of equipment are given in Appendix E.

Monitoring Methodology and QA/QC Procedure

24-hour TSP Monitoring

Operating/Analytical Procedures

2.9 Setup criteria of HVS are shown as follows:

- A horizontal platform with appropriate support to secure the samplers against gusty wind was provided.
- No two samplers were placed less than 2m apart.
- The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2m of separation from walls, parapets and penthouses was set for the rooftop samples.
- A minimum of 2m separation from any supporting structure, measured horizontally was set.
- No furnaces or incineration flues was nearby.
- Airflow around the sampler was unrestricted.
- Any wire fence and gate, to protect the samplers, was not caused any obstruction during monitoring.
- Permission were obtained to setup the samplers and to obtain access to the monitoring stations.
- A secured supply of electricity was provided to operate the samplers.

2.10 Prior to the commencement of the dust sampling, the flow rate of the HVS was properly set (between 1.1 m³/min. and 1.7 m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.

2.11 For TSP sampling, Glass Fiber Filter Media 8" x 10" having a collection efficiency of > 99 % for particles of 0.3 μm diameter were used.

2.12 The power supply was checked to ensure the sampler worked properly and then placed any filter media at the designated air quality monitoring station.

2.13 The filter holding frame was removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.

2.14 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure was sufficient to avoid air leakage at the edges.

2.15 The shelter lid was closed and secured with the aluminium strip.

2.16 The timer was programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).

2.17 After sampling, the filter was removed from the HVS and put into a clean and labeled seal plastic bag to avoid cross contamination. The elapsed time was also be recorded. The sampled filters were sent to the HOKLAS accredited or other internationally accredited laboratory for weighting.

Maintenance/Calibration

2.18 The following maintenance/calibration are required for the HVS:

- The HVS and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
- High volume samplers were calibrated at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

1-hour TSP Monitoring

Measurement Procedures

2.19 The measurement procedures of the 1-hour TSP were conducted in accordance with the Manufacturer's Instruction Manual as follows:

- Set up the dust meter on a tripod at 1.2m level.
- Turned on the dust meter and check the battery, if too low, change new ones. Pointed the meter to the source area or the planned measurement area.
- The zero calibration of the instrument was conducted before and after each sampling.
- TSP levels were recorded for 1-hour with 5-minute data logging interval.
- Recorded down the general meteorological conditions, Test ID no., start/end time, spot check reading at each sampling location for data processing.

- Recorded any activities that may generate dust during measurement period.

Maintenance/Calibration

2.20 The following maintenance/calibration are required for the direct dust meters:

- To validate the accuracy of dust meter, compare the results measured by dust meter and HVS every 12 months throughout all stages of the air quality monitoring.

Wind Data Monitoring

2.21 Wind Anemometer was installed at the roof-top of AM2(A) – Ng Wah Catholic Secondary School with 10m above ground and clear of constructions or turbulence caused by the buildings.

2.22 The wind data was captured by a data logger and the data was downloaded at least once per month for analysis.

2.23 The wind data monitoring equipment will be re-calibrated at least once every six months.

2.24 Wind direction is divided into 16 sectors of 22.5 degrees each.

2.25 Details of weather information during the monitoring period are shown in Appendix F.

Action and Limit Levels

2.26 The Action and Limit Levels of 24-hour average TSP and 1-hour average TSP are summarized in Table 2.4 and Table 2.5 respectively.

Table 2.4 Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
24-hour average TSP	AM2(A)	175	260
	AM3	172	260

Table 2.5 Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hour average TSP	AM2(A)	302	500
	AM3	301	500

Impact Air Quality Monitoring results

2.27 Impact monitoring results for 24-hour average TSP and 1-hour average TSP levels at the designated air quality monitoring stations are summarized in Table 2.6 and Table 2.7 respectively.

Table 2.6 Summary of 24-hour average TSP Monitoring Data during the reporting month

Air Quality Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM2(A)	45	21 – 71	175	260
AM3	62	35 – 95	172	260

Table 2.7 Summary of 1-hour average TSP Monitoring Data during the reporting month

Air Quality Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM2(A)	54	35 – 77	302	500
AM3	55	34 – 78	301	500

2.28 There was no Action and Limit Level exceedance of 24-hour average TSP and 1-hour average TSP levels recorded during the reporting month.

2.29 Graphical presentation and detailed monitoring results of 24-hour average TSP and 1-hour average TSP levels are shown in Appendix G and Appendix H respectively.

2.30 The Event and Action Plan is provided in Appendix I.

2.31 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

2.32 Weather conditions during the monitoring periods were generally fine and did not affect the monitoring results.

2.33 Impact air quality monitoring were conducted on 3, 8, 14, 20 and 26 February 2025 in the reporting month.

3. NOISE MONITORING

Monitoring Requirements

- 3.1 In accordance with EM&A Manual (EIA Register No. AEIAR-130/2009), impact noise monitoring shall be carried out during the construction phase of the Project.
- 3.2 Regular monitoring, $L_{Aeq, 30\text{-minute}}$, for each station will be on a weekly basis and conduct one set of measurements between 0700 – 1900 hrs on normal weekdays.
- 3.3 If construction works are extended to include works during 1900 – 0700 hrs as well as public holidays and Sundays, additional weekly impact monitoring will be carried out during the respective restricted hours periods.

Monitoring Locations

- 3.4 Two designated monitoring stations were selected for noise monitoring programme. Impact noise monitoring was conducted at two noise monitoring stations in the reporting month. Table 3.1 describes the noise monitoring locations, which are also depicted in Figure 6.

Table 3.1 Locations of Noise Monitoring Stations

Noise Monitoring Locations for the Project	Location of Measurement
M4(A) – Le Billionnaire	Podium (Façade)
M5(A) – Prince Ritz	Podium (Façade)

Monitoring Parameters, Frequency and Duration

- 3.5 The noise monitoring locations and monitoring frequency are listed in Table 3.2.

Table 3.2 Noise Monitoring Parameters, Frequency and Duration

Noise Monitoring Station	Location for Measurement	Parameter	Frequency and Duration
M4(A) – Le Billionnaire	Podium (Façade)	L _{Aeq} , L _{A10} and L _{A90}	30-minute measurement at each monitoring station between 0700 – 1900 hrs on normal weekdays (Monday to Saturday) at frequency of once per week.
M5(A) – Prince Ritz	Podium (Façade)		

3.6 The monitoring schedule for reporting month and next month is presented in Appendix C.

3.7 Photographic records of the monitoring setup are shown in Appendix D.

Monitoring Equipment

3.8 As referred to the Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO), sound level meters in compliance with the IEC 61672-1 (Class 1) standard [this standard replaced the International Electrotechnical Commission Publications 60651:1979 (Type 1) and 60804:1985 (Type 1)] were used for noise monitoring. Table 3.3 summarizes the equipment to be used in the noise monitoring.

Table 3.3 Noise Monitoring Equipment

Equipment	Model	Quantity	Calibration Interval
Sound Level Meter	RION NL52	1	1 year
Sound Level Calibrator	RION NC74	2	1 year
Air Flowmeter	TSI TA440 Air Velocity	1	1 year

3.9 Calibration certificates, catalogue of equipment are given in Appendix J.

Monitoring Methodology and QA/QC Procedure

3.10 The noise level measurement was conducted at 1m from the exterior of the nearby noise sensitive receivers building façade and at 1.2m above the ground and facing to the source area or the planned measurement area.

3.11 No noise measurement was conducted in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. Air flow was measured by air flow meter.

3.12 Turned on the sound level meter and check the battery, if too low, change new ones.

3.13 Calibration was conducted immediately prior to and after each noise measurement, the accuracy of the sound level meters was checked by using sound calibrator generating 1,000 Hz with 94dB. Measurement data was found to be valid only if the calibration levels from before and after the noise measurement agreed to within 1.0 dB.

3.14 Noise level was recorded.

3.15 Recorded any activities that may generate noise during measurement period.

Maintenance and Calibration

3.16 The microphone of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.

3.17 The sound level meter and sound calibrator were calibrated annually by HOKLAS accredited laboratory or equivalent.

Action and Limit Levels

3.18 The Baseline Noise Levels and Action and Limit Levels for construction noise is presented in Table 3.4.

Table 3.4 Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring

Time Period	Noise Monitoring Station	Baseline Noise Levels, dB (A)	Action Level	Limit Level [^]
0700 – 1900 hrs on normal weekdays	M4(A)	69.5	When one documented complaint is received.	75 dB(A)
	M5(A)	72.5		

Note: ^ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Impact Noise Monitoring results

3.19 Impact noise monitoring results at the designated noise monitoring stations are summarized in Table 3.5 respectively.

Table 3.5 Summary of Noise Monitoring Data during the reporting month

Noise Monitoring Station	Measured $L_{Aeq, 30-min}$, Average, dB(A)	Measured $L_{Aeq, 30-min}$, Range, dB(A)	Action Level	Limit Level [^]
M4(A)	73.1	72.9 – 73.3	When one documented complaint is received	75 dB(A)
M5(A)	74.4	74.1 – 74.6		

Note: [^] If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

3.20 There was no Action and Limit Level exceedance of $L_{Aeq, 30-min}$ recorded during the reporting month.

3.21 Graphical presentation and detailed monitoring results are shown in Appendix K.

3.22 The Event and Action Plan is provided in Appendix L.

3.23 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

3.24 Weather conditions during the monitoring periods were generally fine and did not affect the monitoring results.

3.25 Impact noise monitoring were conducted 3, 14, 20 and 26 February 2025 in the reporting month.

4. COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS

4.1 The environmental impacts predictions were given in Agreement No. CE 35/2006(CE) Kai Tak Development Engineering Study cum Design and Construction of Advance Works - Investigation, Design and Construction - Kai Tak Development Environmental Impact Assessment Report, EIA Register No. AEIAR-130/2009 for Kai Tak Development (The EIA Report). The EM&A data was compared with the EIA predictions as summarized in Table 4.1 to Table 4.3.

Table 4.1 Comparison of 24-hour average TSP Monitoring Data with EIA predictions

Air Quality Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 24-hour average TSP concentration		Measured 24-hr average TSP in Reporting Month (Feb 2025) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM2(A) - Ng Wah Catholic Secondary School	NA	NA	NA	21 – 71
AM3 - Sky Tower	A40 [^]	106 [^]	138 [^]	35 – 95

Note:

[^] Prediction results are given in the Table 3.13 of the EIA Report (EIAO Register No. AEIAR-130/2009) for Kai Tak Development.

Table 4.2 Comparison of 1-hour average TSP Monitoring Data with EIA predictions

Air Quality Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 1-hour average TSP concentration		Measured 1-hr average TSP in Reporting Month (Feb 2025) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM2(A) - Ng Wah Catholic Secondary School	NA	NA	NA	35 – 77
AM3 - Sky Tower	A40 [^]	217 [^]	247 [^]	34 – 78

Note:

[^] Prediction results are given in the Table 3.13 of the EIA Report (EIAO Register No. AEIAR-130/2009) for Kai Tak Development.

Table 4.3 Comparison of Noise Monitoring Data with EIA predictions

Noise Monitoring Station	NSR No. in EIA report	Predicted Mitigated Construction Noise Levels during Normal Daytime Working Hour L _{Aeq, 30min} , dB(A)	Measured Noise Level in Reporting Month (Feb 2025) L _{Aeq, 30min} , dB(A)
M4(A) – Le Billionnaire	NA	NA	72.9 – 73.3
M5(A) – Prince Ritz	NA	NA	74.1 – 74.6

- 4.2 No prediction in the EIA Report for 24-hour TSP monitoring results at AM2(A).
- 4.3 24-hour TSP monitoring results at AM3 was recorded lower than the prediction in the EIA Report. Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.
- 4.4 No prediction in the EIA Report for 1-hour TSP monitoring results at AM2(A).
- 4.5 1-hour TSP monitoring results at AM3 was recorded lower than the prediction in the EIA Report. Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.
- 4.6 No prediction in the EIA Report for noise monitoring results at M4(A) and M5(A).

5. LANDSCAPE AND VISUAL MONITORING

5.1 In accordance with EM&A Manual (EIA Register No. AEIAR-130/2009), Landscape and Visual Monitoring shall be carried out during the construction phase of the Project. Regular impact monitoring will be conducted at least once per week.

Results and Observations

5.2 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.

5.3 Site inspections were conducted on 6, 13, 20 and 27 February 2025 in the reporting month.

5.4 The summary of site audits is attached in Table 5.1.

Table 5.1 Summary of observations of Landscape and Visual impact during the reporting month

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
6 Feb 2025	NA	NA	NA
13 Feb 2025	NA	NA	NA
20 Feb 2025	NA	NA	NA
27 Feb 2025	NA	NA	NA

5.5 No non-compliance of the landscape and visual impact was recorded in the reporting month.

5.6 Should non-compliance of the landscape and visual impact occur, action in accordance with the action plan presented in Appendix M shall be performed.

6. ENVIRONMENTAL SITE INSPECTION AND AUDIT

Site Inspection





6.1 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.

6.2 Site inspections were conducted 6, 13, 20 and 27 February 2025 in the reporting month.

6.3 The summaries of site audits are attached in Table 6.1.

Table 6.1 Summary of site inspections observations during the reporting month

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
6 Feb 2025	 <p>Observation: C&D waste found shall be removed timely to uphold the site hygiene conditions.</p>	 <p>Action Taken: C&D waste found has been removed timely to uphold the site hygiene conditions.</p>	Closed out on 13 Feb 2025
13 Feb 2025	 <p>Observation: Every vehicle should be washed to remove any dusty materials form its body and wheels before leaving the construction sites.</p>	 <p>Action Taken: Every vehicle has been washed to remove any dusty materials form its body and wheels before leaving the construction sites.</p>	Closed out on 20 Feb 2025

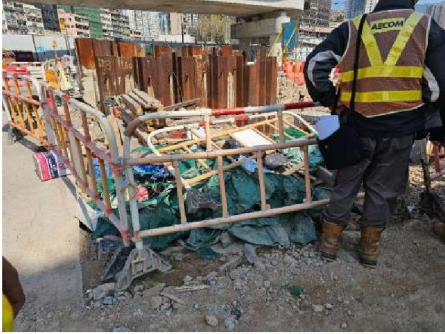Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
20 Feb 2025	 <p>Observation: Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites in L9 road.</p>	 <p>Action Taken: Every vehicle has been washed to remove any dusty materials from its body and wheels before leaving the construction sites.</p>	Closed out on 27 Feb 2025
27 Feb 2025	 <p>Observation: C&D waste found shall be removed timely to uphold the site hygiene conditions.</p>	 <p>Action Taken: C&D waste found has been removed timely to uphold the site hygiene conditions.</p>	Closed out on 6 Mar 2025

Status of Waste Management

- 6.4 The amount of wastes generated by the major site activities of the work contracts within the Project during the reporting month is shown in Appendix N.
- 6.5 The Contractor was registered as a chemical waste producer for the Project. The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

Status of Environmental Licenses, Notification and Permits

6.6 A summary of the relevant permits, licenses and/or notifications on environmental protection for the Project is shown in Table 6.2.

Table 6.2 Summary of Environmental Licenses, Notifications and Permits

Environmental Licenses, Notifications and Permits	Ref. No.	Valid From	Valid Till
Environmental Permit under EIAO	EP-337/2009	23 Apr 2009	N/A
Construction Dust Notification under APCO	HA/1826/1	29 Dec 2020	N/A
Waste Disposal Billing Account	7038086	21 Aug 2020	N/A
Registration as a Chemical Waste Producer	5111-286-B2596-01	15 Sep 2020	N/A
Wastewater Discharge License under WPCO	WT00037618-2021	29 Mar 2021	31 Mar 2026
	WT00037370-2021		
	WT00038562-2021	15 Jul 2021	31 Jul 2026
Construction Noise Permit	GW-RE1228-24	20 Oct 2024	30 Mar 2025
	GW-RE1595-24	14 Dec 2024	25 Feb 2025

Implementation Status of Environmental Mitigation Measures

6.7 The Contractor has implemented environmental mitigation measures as stated in the EIA report, the EP and the EM&A Manual. The implementation status of the mitigation measures is summarized in Appendix O.

Environmental Complaint and Non-compliance

6.8 No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table 6.3.

Table 6.3 Summary of complaints in the Reporting Month

Date of complaint received	Date of complaint	Description of complaint	Recommendations / Action taken	Close-out date / Status
No complaint was received in the reporting month.	NA	NA	NA	NA

6.9 Complaint log is shown in Appendix P.

Notifications of summons and successful prosecutions

6.10 No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table 6.4.

Table 6.4 Summary of summons and successful prosecutions in the Reporting Month

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
No notification of summons and successful prosecutions were received in the reporting month.	NA	NA	NA	NA

6.11 The summaries of cumulative environmental complaint, warning, summons and notification of successful prosecution for the Project is presented in Appendix P.

7. FUTURE KEY ISSUES

Construction Programme in the coming month

7.1 The major construction activities and potential impacts in the next reporting month are as follows:

Table 7.1 Summary of future key issues and potential impact in the coming month

Future key issues in the coming month	Potential impact
Installation of E&M equipment for pillar box at LW-02	Noise and Air Quality
Lift installation at LW-02	Noise and Air Quality
Installation of glass panels and aluminum panels of LW-02	Noise and Air Quality
Installation of glass balustrade at LW02	Noise and Air Quality
Planting works at LW02	Noise and Air Quality
Tiling works at LW02	Noise and Air Quality
Construction of Parapet for S14	Noise and Air Quality
Refurbishment works for Bridge K73	Noise and Air Quality
Construction of bridge deck of S14	Noise and Air Quality
Drainage construction works at PS2	Noise and Air Quality
Construction of end wall at Subway SB-01 Retrieval Shaft	Noise and Air Quality
Finishing works of Subway SB-01	Noise and Air Quality
Construction of top slab of lift tower at Subway SB-01	Noise and Air Quality
Demolition of accessible ramp inside SB01	Noise and Air Quality
Excavation works for construction of staircase at Subway SB-01	Noise and Air Quality
Tiling works for Subway SB-01	Noise and Air Quality
Road and drain construction works for Road L16, Road L9 and Road D1 and	Noise and Air Quality
Construction works for DCS	Noise and Air Quality

7.2 The mitigation measures for environmental impact including Air Quality, Construction Noise, Water Quality, Chemical and Waste Management, Landscape and Visual shall be implemented:

- Sufficient watering of the works site with the active dust emitting activities,
- Limitation of the speed for vehicles on unpaved site roads,
- Properly cover the stockpiles,
- Good maintenance to the plant and equipment,
- Use of quieter plant and Quality Powered Mechanical Equipment (QPME),
- Provide movable noise barriers,
- Appropriate desilting/ sedimentation devices provided on site for treatment before discharge,
- Well maintain the drainage system to prevent the spillage of wastewater during heavy rainfall,
- Onsite waste sorting and implementation of trip ticket system,

- Good management and control on construction waste reduction,
- Erection of decorative screen hoarding,
- Strictly following the Environmental Permits and Licenses, and
- Provide sufficient mitigation measures as recommended in Approved EIA Report.

7.3 The recommended environmental measures proposed in the EM&A Manual (EIA Register No. AEIAR-130/2009) shall be effectively implemented to minimize the potential environmental impacts. The Contractor is reminded to implement the mitigation measures properly.

Environmental Site Inspection and Monitoring Schedule for next month

7.4 The tentative schedule for weekly site inspection and air quality and noise monitoring in the next month is provided in Appendix C.

8. CONCLUSIONS

- 8.1 Environmental monitoring works were performed in the reporting month and all monitoring results were checked and reviewed.
- 8.2 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.3 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.4 Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.5 No complaint was received in the reporting month.
- 8.6 No notification of summons and successful prosecutions was received in the reporting month.
- 8.7 Based on the site inspection and audits, impact air quality and noise monitoring results, it was considered that the mitigation measures were effective to control the potential environmental impacts from the Project during the reporting period.

Figure

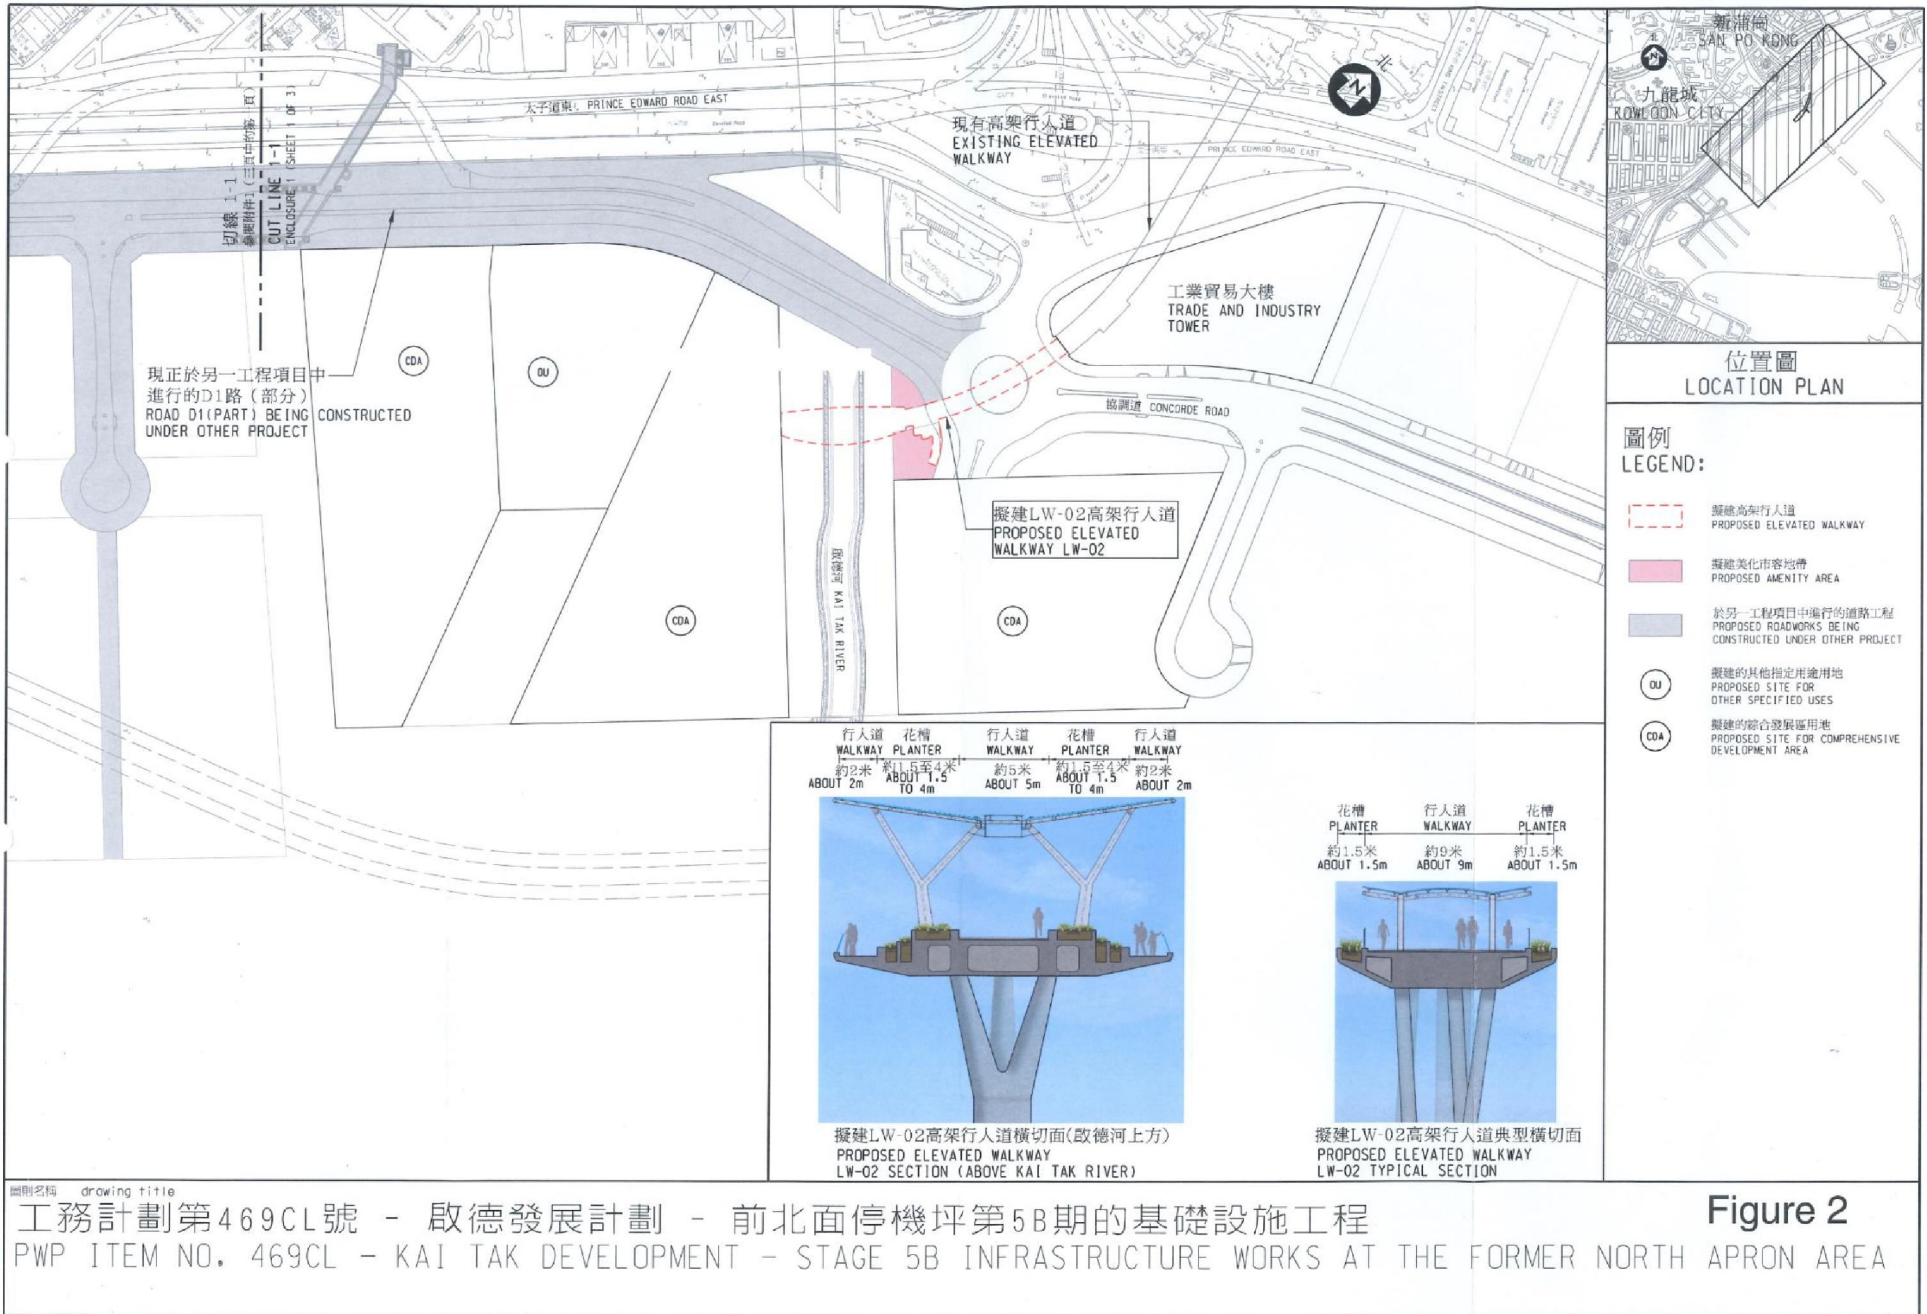


Figure 2 – Proposed works of Contract No. ED/2018/05

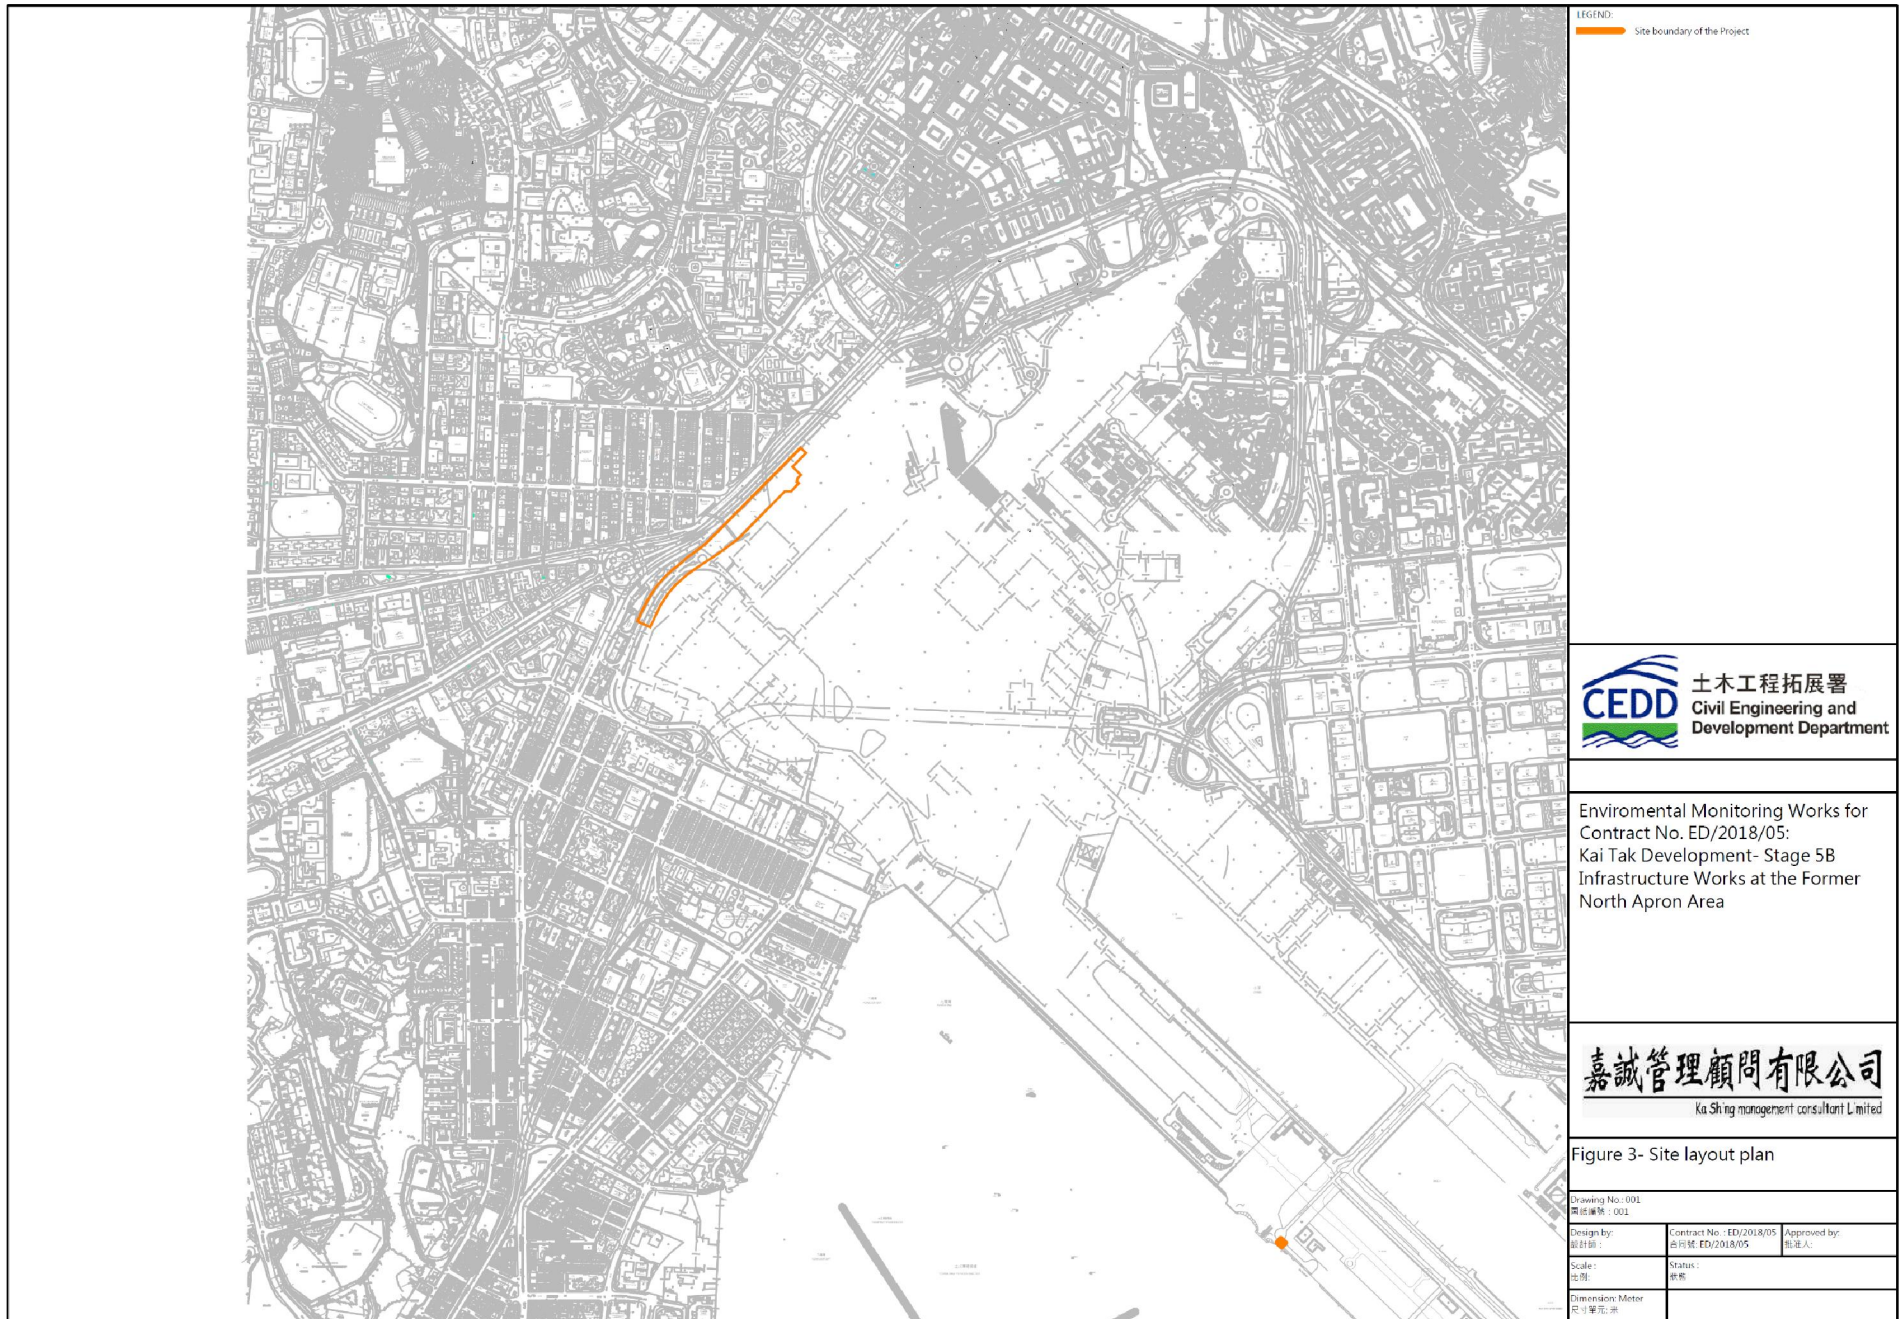


Figure 3 – D1 Road Site Layout Plan

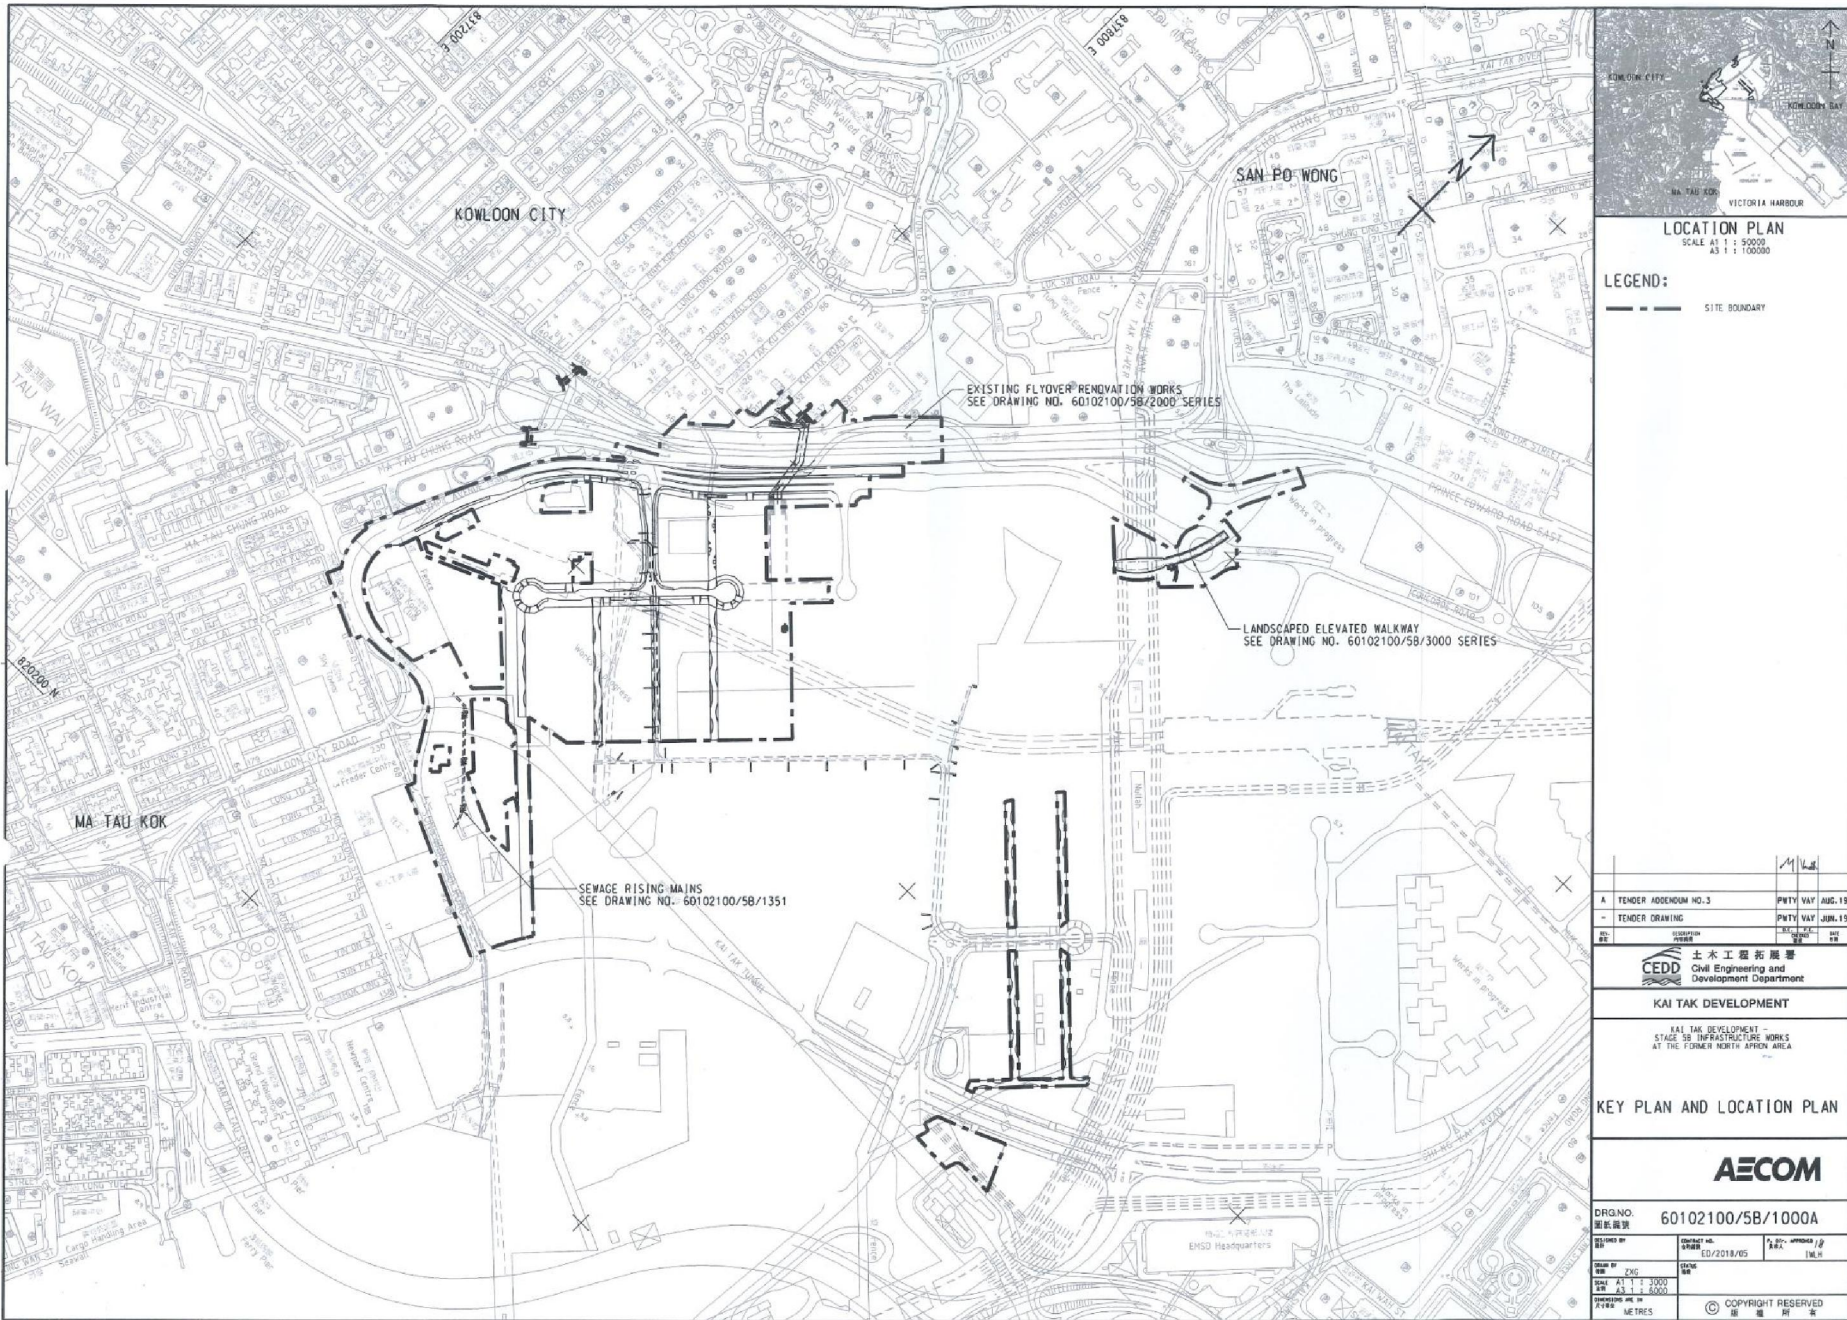


Figure 4 – Site Layout Plan

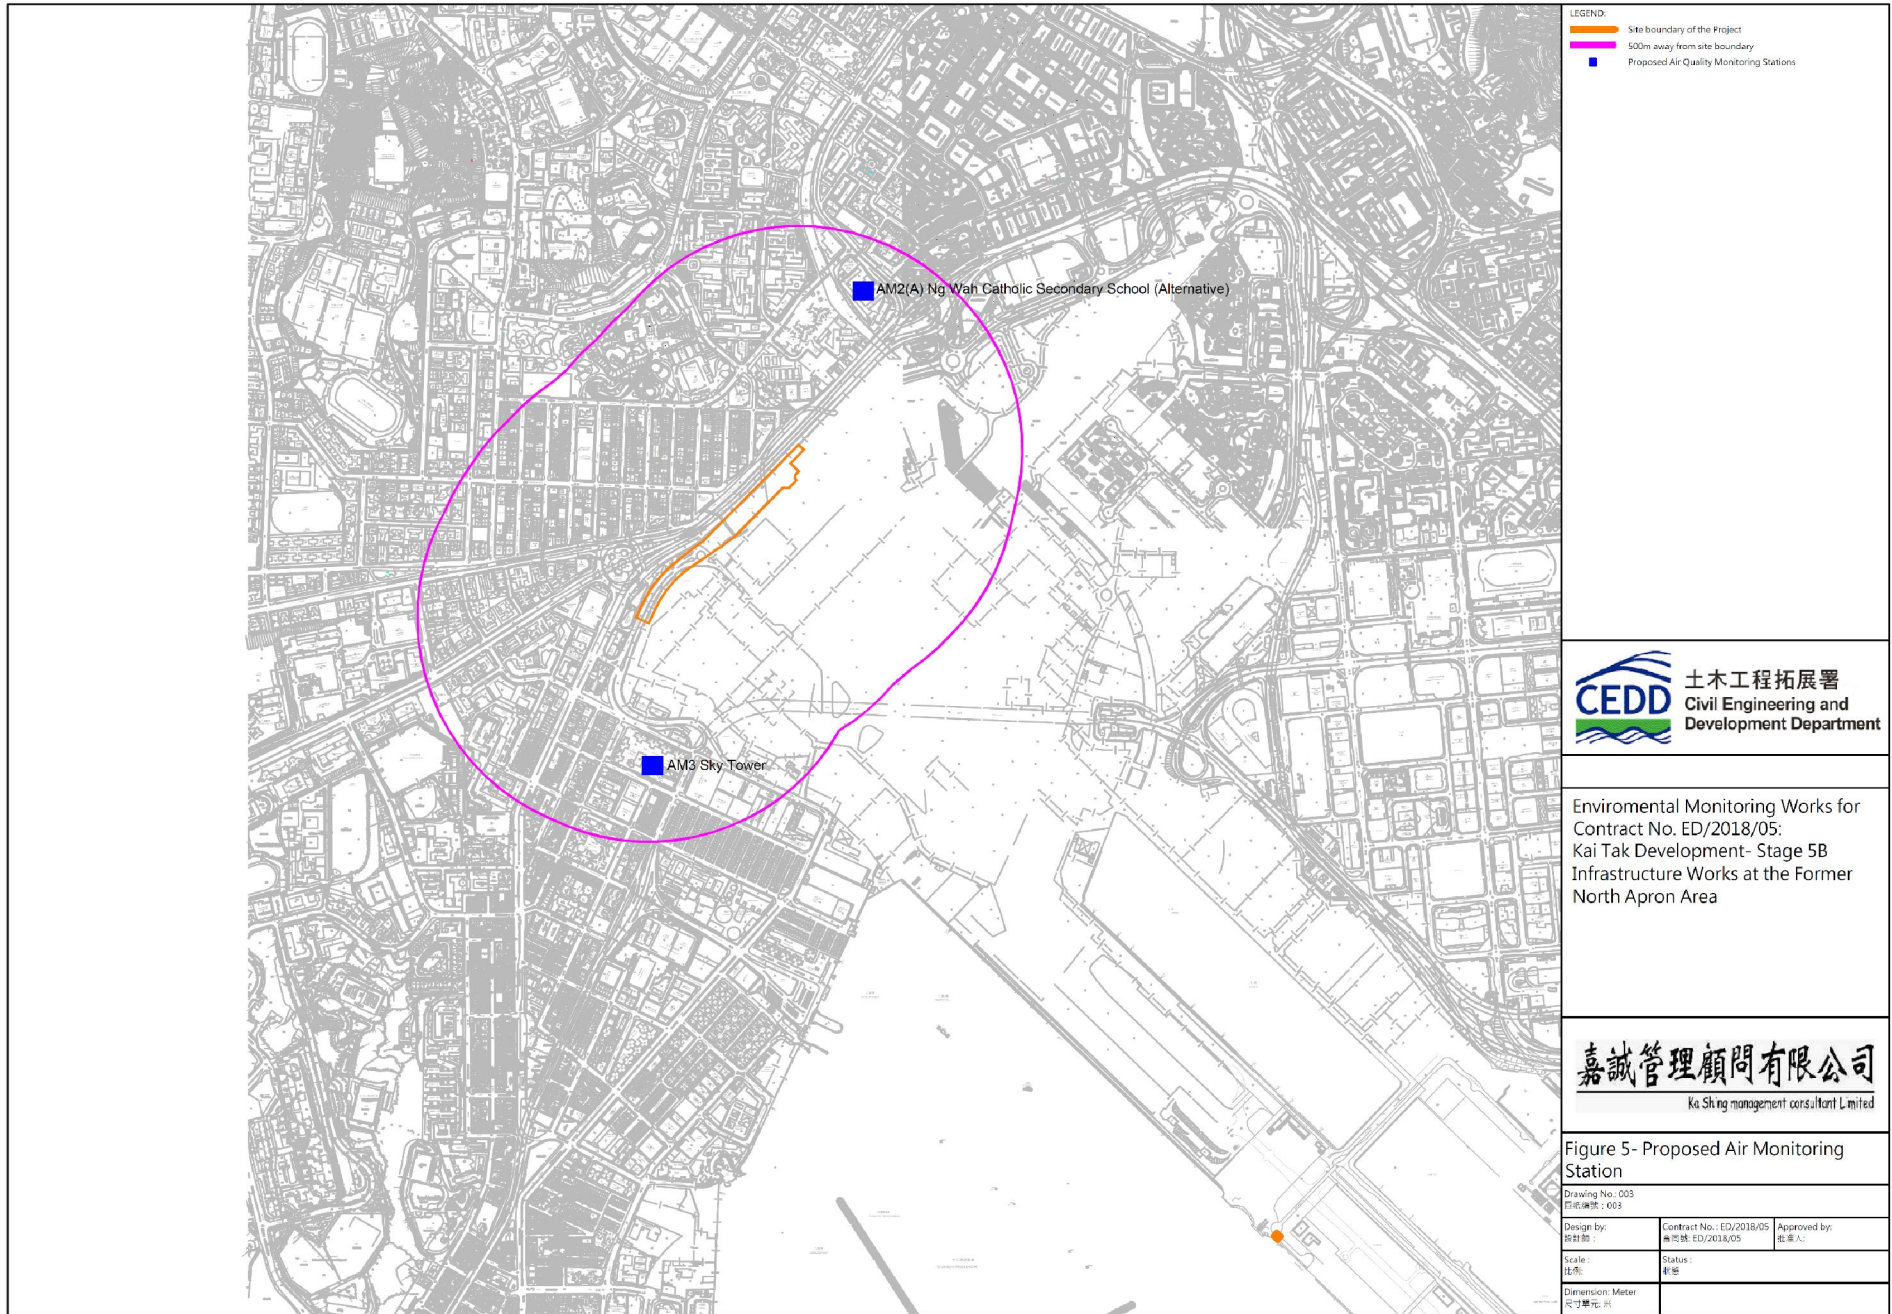


Figure 5 – Air Quality Monitoring Stations

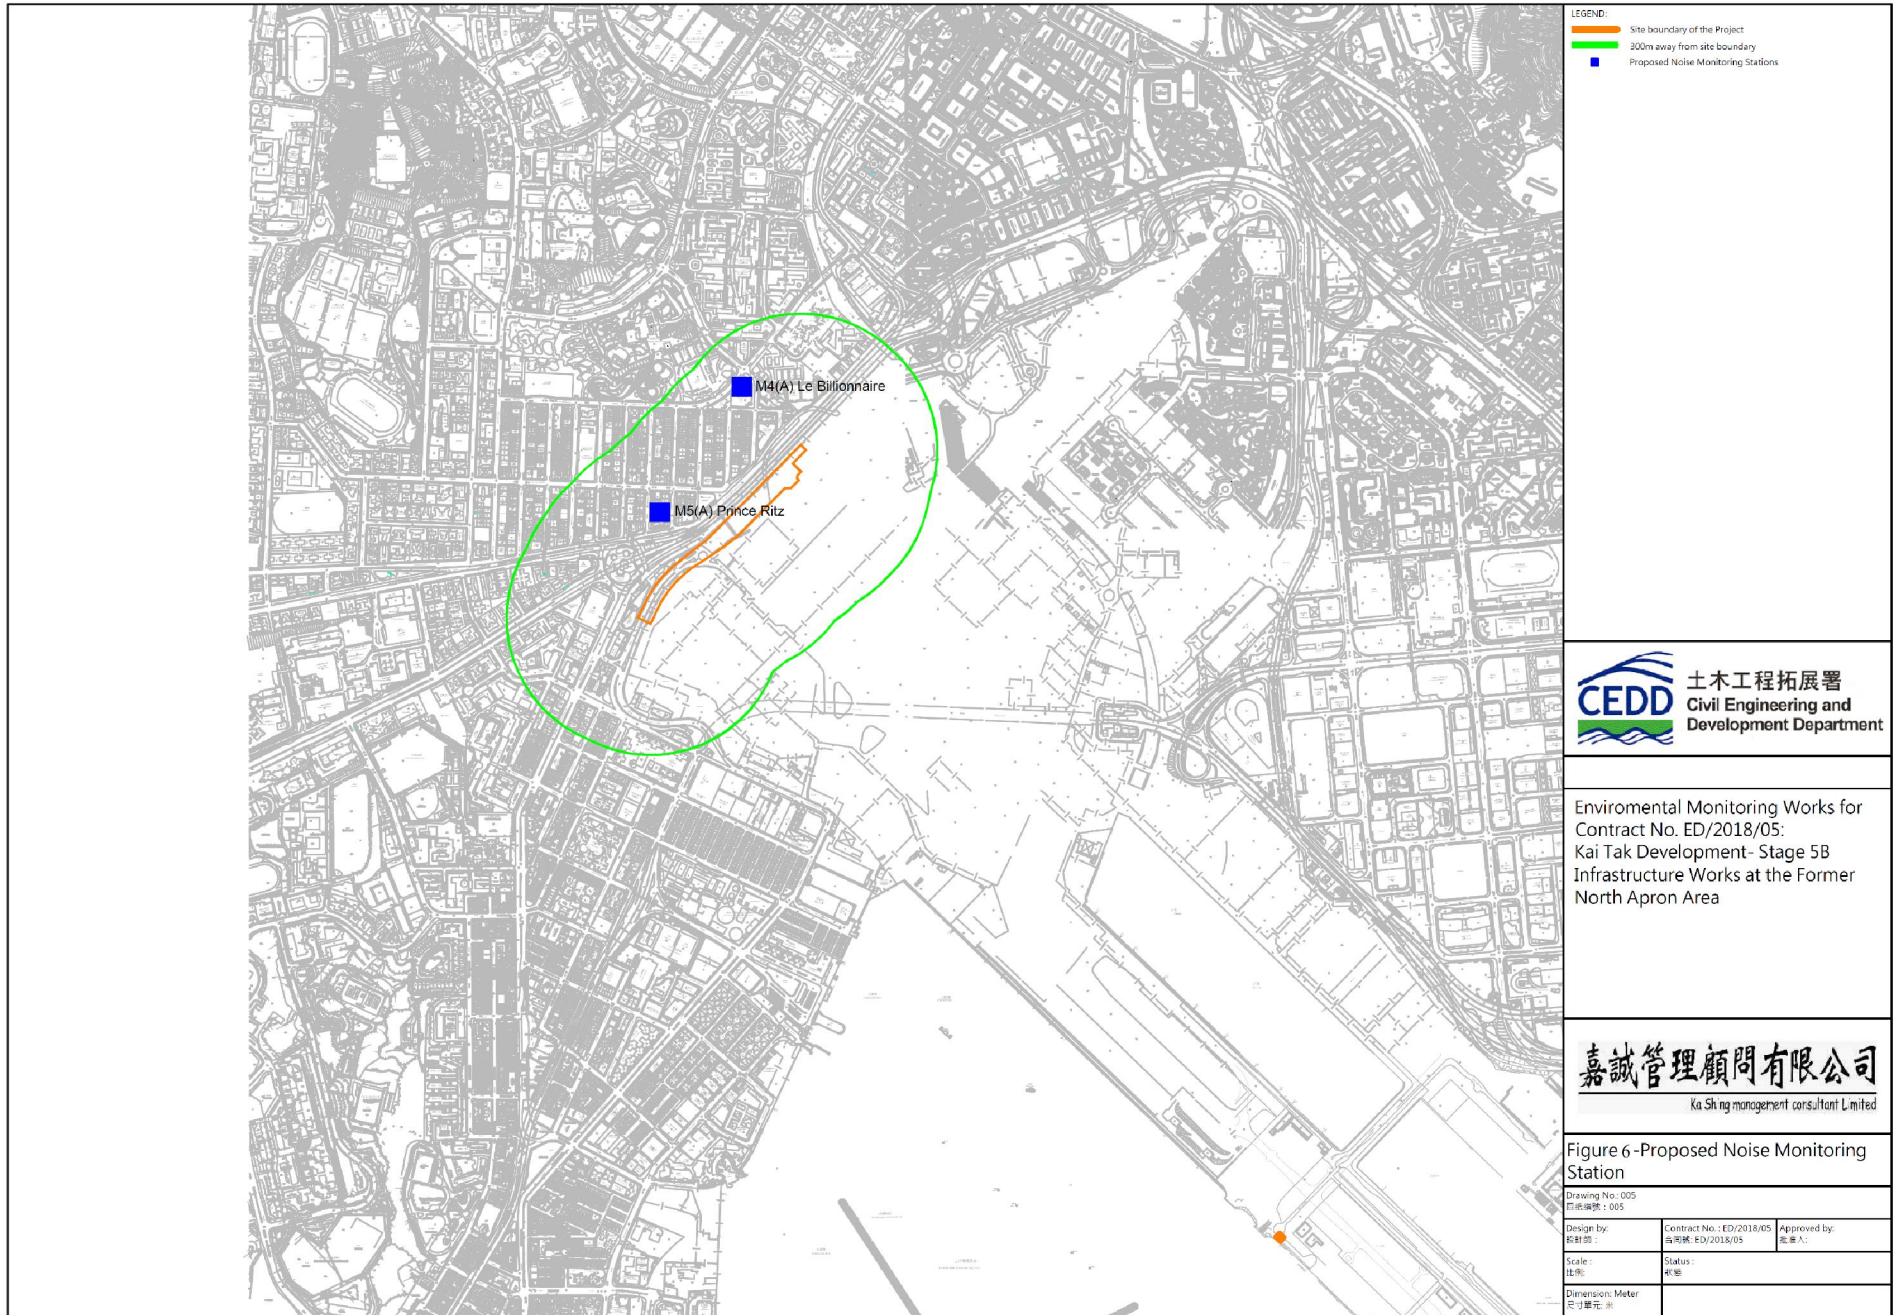


Figure 6 – Noise Monitoring Stations

Appendix A – Organization Chart of EM&A Team

Appendix B – Construction Programme

Appendix C – Environmental monitoring schedules

Contract No. EDO 2/2020 Environmental Monitoring at Kai Tak Development – Stage 5B infrastructure works at the former north apron area
Environmental Monitoring and Weekly Site Inspection Schedule for February 2025

February 2025

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1
2	3 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	4	5	6 Weekly Site Inspection	7	8 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3
9	10	11	12	13 Weekly Site Inspection	14 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	15
16	17	18	19	20 Weekly Site Inspection 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	21	22
23	24	25	26 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	27 Weekly Site Inspection + SSMC meeting	28	

Air Quality Monitoring Station
AM2(A) Ng Wah Catholic Secondary School
AM3 - Sky Tower

Noise Quality Monitoring Station
M4(A) - Le Billionnaire
M5(A) - Prince Ritz

Contract No. EDO 2/2020 Environmental Monitoring at Kai Tak Development – Stage 5B infrastructure works at the former north apron area
Tentative Environmental Monitoring and Weekly Site Inspection Schedule for March 2025

March 2025

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1
2	3	4 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	5	6 Weekly Site Inspection	7	8
9	10 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	11	12	13 Weekly Site Inspection	14	15 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3
16	17	18	19	20 Weekly Site Inspection	21 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	22
23	24	25	26	27 Weekly Site Inspection+ SSMC meeting 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	28	29
30	31					

NOTE:

1) Site inspection schedule and Impact monitoring schedule may be changed due to unforeseen circumstance (e.g. adverse weather).

Air Quality Monitoring Station

AM2(A) Ng Wah Catholic Secondary School

AM3 - Sky Tower

Noise Quality Monitoring Station

M4(A) - Le Billionnaire

M5(A) - Prince Ritz

Appendix D – Photographic records

Impact Air Quality Monitoring



Measurement setup at AM2(A)



Measurement setup at AM3



Weather Station at the rooftop of Ng Wah Catholic Secondary School

Impact Noise Monitoring



Measurement setup at M4(A)



Measurement setup at M5(A)

Appendix E – Calibration certificates, catalogue of air quality monitoring equipment

Catalogue of High Volume Sampler (HVS)



TSP MFC

Total Suspended Particulate, Mass Flow Controlled

MFC TSP

Ambient Air Sampler

The TE-5170 is a high volume ambient Total Suspended Particulate (TSP) air sampler featuring a mass flow controller (MFC) for accurate and consistent particulate sampling. The mass flow controller adjust the motor speed as the filter media collects particulate to maintain a constant flow rate throughout the entire sample duration. The system utilizes a stainless steel filter holder for use with standard 8" x 10" filter paper. The anodized aluminum shelter and robust electrical components allow the system to operate a continuous 24 hour sample.

ABOUT US: Tisch Environmental Inc. Tisch Environmental is the benchmark for high volume air sampling, particulate, metals, volatiles, and specialty monitoring equipment. Since the company's inception in 1953 as General Metal Works, our product line has expanded from the first high volume air sampler to include high-tech and custom samplers. Our clients are professionals from every sector of the regulatory and industrial markets.

- ✔ Meets EPA CFR, Appendix B to Part 50
- ✔ Total Suspended Particulate(TSP)
- ✔ Mass Flow Controlled
- ✔ 7-Day Mechanical Timer
- ✔ Elapsed Time Indicator
- ✔ Aluminum Outdoor Shelter
- ✔ Brush Style Motor
- ✔ Dickson Chart Recorder, 24 Hour
- ✔ Stainless Steel Filter Holder
- ✔ 36-60 CFM
- ✔ Made In USA



TSP MFC

MFC TSP Ambient Air Sampler

General System Specifications

Particulate Size:Total Suspended Particulate (TSP)
EPA Designation: CFR 40 Part 50 Appendix B
Flow Controller: Mass Flow Controller
Motor Style:Brush Style Motor Assembly
Pressure Recorder:Dickson Chart Recorder, 24 hour
Timer:7 Day Mechanical
Elapsed Time Indicator:Mechanical, Hours and Tenths
Flow Range:39-60CFM, 1.09M³M-1.68M³M
Housing:Anodized Aluminum
Filter Holder:Stainless Steel, 8" x 10"
4" Recorder Charts: Box of 100
Filter Holder: 8" x 10" Stainless Steel with hold down frame

Applications

US EPA Reference Method Sampling, CFR Appendix J Part 50 Regulatory Compliance
 Institutional Studies
 Construction Sites
 Bridge and Water Tower Painting Sites
 Fence Line Monitoring
 Industrial Monitoring
 Landfill Monitoring
 Public Health Applications

Optional Equipment

TE-3000 Filter Holder Cartridge
 TE-G653 8" x 10" Glass Fiber Filter Media
 TE-33384 Motor Brush Set (110volt)
 TE-33378 Motor Brush Set (220volt)
 TE-116311 Replacement Motor (110volt)
 TE-116312 Replacement Motor (220volt)
 TE-106 Recorder Charts
 TE-160 Recorder Pen Points
 TE-5018 Gasket 8" x 10"

Available Models

TE-5170 TSP MFC, 110 Volt 60 Hertz, 8 Amps
 TE-5170X TSP MFC, 220 Volt 50 Hertz 4 Amps
 TE-5170XZ TSP MFC, 220 Volts 60 Hertz, 4 Amps

Calibration Equipment

TE-5028 -Variable Flow Calibration Kit
 TE-HVC-V Xcalibrator HiVol Calibrator

Physical Specifications

Weight: 75lbs, Shelter
Shipping Dimensions: 46"W x 23"L x 20" H, Shelter
 19"W x 19"L x 20"H, Lid
Assembled Dimensions: 28"W x 28"L x 61"H

Calibration Certificate of HVS

Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2025020104 Date of calibration : 01/02/2025

Model no : Ng Wah Catholic Secondary School Sampler : TE-5170X
Serial Number : 4360

Calibration Data

Ambient barometric pressure, Pa = 759.8 (mmHg) Ambient temperature, Ta = 294.55 (deg K)

Calibration Orifice


Model = TE-5025A Qstd Slope, m = 2.03976
Serial No. = 0006 Qstd Intercept, b = -0.01299
Calibration Due Date: 06/05/2025 Qstd Corr. coeff., r = 1.00000

Calibration Curve

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	7.80	1.383	49.0	49.28
13	6.60	1.273	44.0	44.25
10	4.40	1.041	37.0	37.21
7	3.30	0.902	32.0	32.18
5	2.20	0.738	26.0	26.15

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1 / ml [(1) (\text{Sqrt} ((Pa / 760) (298 / Ta))) - b1]$	34.952	0.5061	0.9987

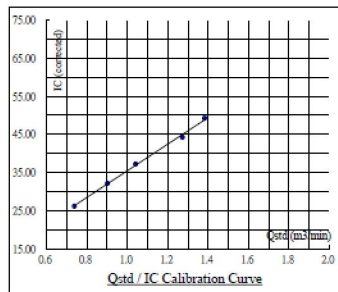

Calibration curve requirements : (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³ / min).

Remark : $Qstd (m^3 / min) = 1/ml [\text{Sqrt} (H_2O (Pa / 760) (298 / Ta)) - b]$.

$IC (corrected) = I [\text{Sqrt} ((Pa / 760) (298 / Ta))]$.

$FLOW (corrected) = \text{Sqrt} (FLOW (mano) (Pa / 760) (298 / Ta))$.

Calibrated by : Ben Poon 01/02/2025 Checked by : Chris Choy 01/02/2025

Name : (Ben Poon) Name : (Chris Choy)

Form No. INS-HVS-CAL-44 16 01 2020

Calibration Certificate of HVS

Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2025020101 Date of calibration : 01/02/2025

Model no : Sky Tower Sampler : TE-5170X
Serial Number : 4687

Calibration Data

Ambient barometric pressure, Pa = 759.8 (mmHg) Ambient temperature, Ta = 294.55 (deg K)

Calibration Orifice


Model = TE-5025A Qstd Slope, m = 2.03976
Serial No. = 0006 Qstd Intercept, b = -0.01299
Calibration Due Date: 06/05/2025 Qstd Corr. coeff., r = 1.00000

Calibration Curve

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	7.80	1.383	50.0	50.29
13	6.60	1.273	44.0	44.25
10	4.50	1.052	37.0	37.21
7	3.30	0.902	32.0	32.18
5	2.10	0.721	26.0	26.15

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1 / ml [(1) (\text{Sqrt} ((Pa / 760) (298 / Ta))) - b1]$	35.389	0.2845	0.9965

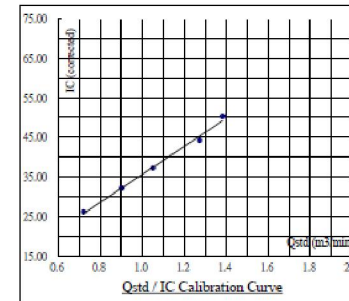

Calibration curve requirements : (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³ / min).

Remark : $Qstd (m^3 / min) = 1/ml [\text{Sqrt} (H_2O (Pa / 760) (298 / Ta)) - b]$.

$IC (corrected) = I [\text{Sqrt} ((Pa / 760) (298 / Ta))]$.

$FLOW (corrected) = \text{Sqrt} (FLOW (mano) (Pa / 760) (298 / Ta))$.

Calibrated by : Ben Poon 01/02/2025 Checked by : Chris Choy 01/02/2025

Name : (Ben Poon) Name : (Chris Choy)

Form No. INS-HVS-CAL-44 16 01 2020

Calibration Certificate of HVS used for performance check of Dust Meter

Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No.: ATSPC-01-2024053002 Date of calibration: 30/05/2024


Model no.: GS2310 Serial number: 10346

Calibration Data
Ambient barometric pressure, Pa = 753.9 (mmHg) Ambient temperature, Ta = 298.65 (deg K)

Calibration Orifice
Model = TE-5025A Qstd Slope, m = 2.03976
Serial No. = 0006 Qstd Intercept, b = -0.01299
Calibration Due Date: 06/05/2025 Qstd Corr. coeff., r = 1.00000

Plate No.	H ₂ O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)
18	7.60	1.351	50.0	49.74
13	6.50	1.250	44.0	43.77
10	4.40	1.029	38.0	37.81
7	3.20	0.879	32.0	31.84
5	2.20	0.730	27.0	26.86

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1/m [(1) (\text{Sqrt} ((Pa / 760) (298 / Ta))) - b]$	35.445	0.8648	0.9952

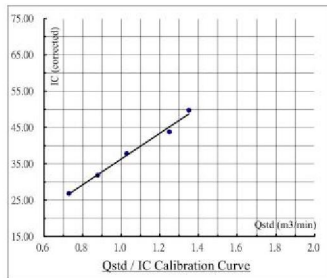

Calibration curve requirements: (A). $r > 0.990$; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m³/min).

Remark: $Qstd (m^3/min) = 1/m [\text{Sqrt} (H_2O (Pa / 760) (298 / Ta)) - b]$
 $IC (corrected) = 1 [\text{Sqrt} ((Pa / 760) (298 / Ta))]$
 $FLOW (corrected) = \text{Sqrt} (FLOW (mano) (Pa / 760) (298 / Ta))$

Calibrated by: Ben Poon 30/05/2024 Checked by: Chris Choy 30/05/2024

Form No. BS-HVS-CAL-01 (16/01/2020)

Orifice Transfer Standard Certification Worksheet TE-5025A

AST-159C-01 Cal date: 6 May 2024



RECALIBRATION DUE DATE:
May 6, 2025

Certificate of Calibration

Calibration Certification Information			
Cat. Date: May 6, 2024	Rootmeter S/N: 438320	Ta: 295 °K	
Operator: Jim Tisch		Pa: 748.5 mm Hg	
Calibration Model #: TE-5025A	Calibrator S/N: 0006		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4190	3.2	2.00
2	3	4	1	1.0030	6.4	4.00
3	5	6	1	0.8950	7.9	5.00
4	7	8	1	0.8520	8.8	5.50
5	9	10	1	0.7040	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H (\frac{Pa}{Pstd}) (\frac{Tstd}{Ta})}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H (Ta / Pa)}$ (y-axis)
0.9907	0.6982	1.4106	0.9957	0.7017	0.8878
0.9864	0.9835	1.9949	0.9914	0.9885	1.2556
0.9844	1.0999	2.2304	0.9894	1.1055	1.4037
0.9832	1.1540	2.3393	0.9882	1.1599	1.4723
0.9781	1.3893	2.8213	0.9830	1.3964	1.7756
QSTD	m= 2.03976		QA	m= 1.27726	
	b= -0.01299			b= -0.00818	
	r= 1.00000			r= 1.00000	

Calculations	
$Vstd = \Delta Vol / ((Pa - \Delta P) / Pstd) (Tstd / Ta)$	$Va = \Delta Vol / ((Pa - \Delta P) / Pa)$
$Qstd = Vstd / \Delta Time$	$Qa = Va / \Delta Time$
For subsequent flow rate calculations:	
$Qstd = 1/m (\sqrt{ \Delta H (\frac{Pa}{Pstd}) (\frac{Tstd}{Ta}) } - b)$	$Qa = 1/m (\sqrt{ \Delta H (Ta / Pa) } - b)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH:	calibrator manometer reading (in H2O)
ΔP:	rootmeter manometer reading (mm Hg)
Ta:	actual absolute temperature (°K)
Pa:	actual barometric pressure (mm Hg)
b:	intercept
m:	slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
145 South Miami Avenue
Village of Cleves, OH 45002

www.tisch-env.com
TOLL FREE: (877)263-7610
FAX: (513)467-9009

Catalogue of Dust Meter (TSI Sidepak AM510)

The SidePak AM510 monitor's easy-to-read display shows your data as both real-time aerosol mass-concentration and 8-hour time-weighted average (TWA). With its convenient data logging and long battery life, the AM510 is also ideal for extended sampling. The easy-to-use TrakPro Data Analysis Software lets you create effective graphs and reports.



User Friendly

- + Small, lightweight and quiet to maximize worker acceptance
- + Rugged design with secure belt clip
- + Easy-to-understand user interface with only four keys
- + Lockable keypad prevents tampering while sampling
- + User-adjustable sample flow rate
- + Define, label and store multiple calibration constants
- + Easy-to-read LCD display
- + Convenient, threaded tripod socket accommodates area sampling

Advanced Features

- + Smart Battery Management System provides precise run time information, maximizes battery capacity and speeds charging
- + Integrated pump allows use of size-selective aerosol inlet conditioners
- + Built-in impactors let you choose "none," 1.0, 2.5 or 10-micron cut off
- + 10-mm Dorr-Oliver cyclone for respirable sampling
- + Display shows real-time concentrations (mg/m³) and "on-the-fly" TWA as you data log
- + Display statistics: max, min and average readings, elapsed time and 8-hour TWA

Quick and Easy Reports

- + Convenient preprogramming for occupational exposure sampling
- + Data log for long periods and store multiple tests
- + Analyze data, print graphs and create reports with TrakPro Data Analysis Software
- + USB port lets you conveniently connect to your computer

Power to Spare

- + Long-lasting NiMH rechargeable battery packs eliminate "memory" issues
- + Choice of rechargeable NiMH smart battery packs or AA-cell pack

Model AM510 SidePak Personal Aerosol Monitor

Sensitivity	
Sensor Type	90° light scattering, 670 nm laser diode
Aerosol Concentration Range	0.001 to 20 mg/m ³ (calibrated to respirable fraction of ISO 12103-1, A1 test dust)
Particle Size Range	0.1 to 10 micrometer (µm)
Minimum Resolution	0.001 mg/m ³
Zero stability	±0.001 mg/m ³ over 24 hours using 10-second time-constant
Temperature Coefficient	Approximately +0.0005 mg/m ³ per °C (for variations from temperature at which instrument was last zeroed)
Flow Rate	
Range	User-adjustable, 0.7 to 1.8 liters/min (L/min)
Temperature Range	
Operating Range	32 to 120°F (0 to 50°C)
Storage Range	-4 to 140°F (-20 to 60°C)
Operational Humidity	
	0 to 95% RH, non-condensing
Time Constant (LCD display)	
Range	User-adjustable, 1 to 60 seconds
Data Logging	
Data Points	Approx. 31,000
Logging Interval	User-adjustable, 1 second to 1 hour
User-Select Calibration Factors	
Factory Setting	1.0 (non-adjustable)
User-defined Settings	3, with user-defined labels
Range	0.1 to 10.0, user-adjustable
Physical	
External Dimensions	4.2 x 3.7 x 2.8 in. (106 x 92 x 70 mm) with 801723, 801724, 801729 or 801743 battery 5.1 x 3.7 x 2.8 in. (130 x 92 x 70 mm) with 801708, 801722, 801728, 801735, or 801736 battery 16 oz (0.46 kg) with 801723, 801724, 801729 or 801743 battery 19 oz (0.54 kg) with 801708, 01722, 801728, 801735, or 801736 battery
Weight	2 line x 12 character LCD
Display	1/4-20 female thread
Tripod Socket	
Power Supply/Charger (P/N 2613210)	
Input Voltage Range	100 to 240 VAC, 50 to 60 Hz
Output Voltage	9 VDC @ 1.0 A

Maintenance

Factory Clean/Calibrate	Recommended annually
User Zero Calibration	Before each use
User Flow Calibration	As needed

Communications Interface

Type	USB 1.1
Connector, Instrument	USB Mini-B (socket)

Minimum Computer Requirements for TrakPro™ Data Analysis Software

Communications Port	Universal Serial Bus (USB) v 1.1 or higher
Operating System	Microsoft Windows® XP, or 7 (32-bit or 64-bit) operating systems

Battery Performance

Battery Options	Charge Time (hrs)*	Intrinsic Safety Rating	Run Time (hrs @ 1.7 L/min)
1600 mAh NiMH Pack, 4.8 V (P/N 801723)	3.0	No	7.1
1650 mAh NiMH Pack, 4.8V (P/N 801724, 801729 or 801743)	3.5	CSA**	7.5
2700 mAh NiMH Pack, 4.8 V (P/N 801722 or 801728)	5.5	No	12.0
2700 mAh NiMH Pack, 4.8 V (P/N 801735)	5.5	No	12.0
6-Cell AA-size Alkaline Pack*** (P/N 801708 or 801736 with six user-supplied AA cells)	N/A	No	22.5

*Of a fully depleted battery
**All dust plugs and dust gaskets must be installed.
***Using Energizer AA-size, E31 alkaline batteries.

Battery Level Indicator

The Smart Battery Management System™ technology utilizes a built-in "gauge" in the SidePak™ battery packs. The gauge monitors battery capacity and calculates run time information by dividing capacity of the battery (mAh) by the instantaneous current consumed by the instrument (mA). This calculation is correct for current operating conditions and can change due to current (mA) consumption or changes in battery capacity.

Calibration Certificate of Dust Meter (TSI Sidepak AM510)



Cal Lab Limited 校正實驗室有限公司
 Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
 Tsuen Wan, NT, Hong Kong
 Tel: +852 25680106 Email: info@callab.com.hk
 Fax: +852 30116194 Website: www.callab.com.hk



Calibration Certificate No.: CC0012408

Information provided by customer

Customer: Castco Testing Centre Limited
 Address: 33, On Kui Street, Fanling, N.T.

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Aerosol Monitor	TSI	SidePak AM510	11208032	AAST-RSP-01

Certificate Information

Date of Receipt:	1 August 2024	Calibration Condition:	24.3°C, 57%RH, 999hPa
Date of Calibration:	16 August 2024	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	ISO 21501-4:2018	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Aerosol Monitor	8534	8534182605	24 November 2024

Result of Calibration

Gas	Reference Setting (mg/m ³)	Measured reading (mg/m ³)	Error (%)	Uncertainty (%)	Technical Requirement	Technical Reference Doc.
Dust - PM10	0.102	0.100	-2.0	17.0	± 10%	Mfr's Spec
Dust - PM10	0.198	0.199	0.5	17.0	± 10%	Mfr's Spec
Dust - PM10	0.304	0.305	0.3	17.0	± 10%	Mfr's Spec

CF-GAS-01

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
 Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
 Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
 Note4: The result shown in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.
 Note5: Calibration item/ parameter marked with * is out of scope of Cal Lab Limited (A2/LA 3815.01).

Calibrated By:

Wing Cheng

Wing Cheng

Checked and Approved By:

Warren Yeung

Warren Yeung

Company Chop:



Certificate Issue Date: 19 August 2024

CF-BEG-04

*** End of Certificate ***

1. The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
 2. The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0012408
 Page 1 of 1

Personal Aerosol Monitor Performance check with High Volume Sampler

Performance Check ref. No. AS0240523-1 Report Issue Date 23/05/2024
 Date of performance check 23/05/2024

Objective:


A dust meter and a Total Suspended Particulate High Volume Air Sampler (HVS) were placed together to measure the Total Suspended Particulate (TSP) concentrations simultaneously to check the performance.

Equipment Used:

Equipment	Manufacturer and Model	Serial Number
Personal Aerosol Monitor	TSI AM510 Sidepak	11208032
Total Suspended Particulate High Volume Air Sampler	GS2310	10346

Result:

Equipment	Measurement Result, µg/m ³			
TSI AM510 Sidepak	64	142	224	336
High Volume Air Sampler (HVS)	41	116	181	267

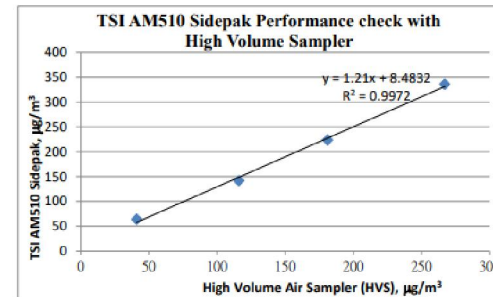

Tested by:

(*Poon Tsz Wing*)

Form No. ENV CAL SAMPLER CCT 4412/12/2003

Checked by:

(*Choy Ching Yee*)

Calibration Certificate of Dust Meter (TSI Sidepak AM510)



Cal Lab Limited 校正實驗室有限公司
 Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
 Tsuen Wan, NT, Hong Kong
 Tel: +852 25680106 Email: info@callab.com.hk
 Fax: +852 30116194 Website: www.callab.com.hk



Cal Date: 16 Aug 2024

Calibration Certificate No.: CC0022408

Information provided by customer

Customer: Casco Testing Centre Limited
 Address: 33, On Kui Street, Fanling, N.T.

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Aerosol Monitor	TSI	SidePak AM510	11506014	AAST-RSP-09

Certificate Information

Date of Receipt:	1 August 2024	Calibration Condition:	24.3°C, 57%RH, 999hPa
Date of Calibration:	16 August 2024	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	ISO 21501-4:2018	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Aerosol Monitor	8534	8534182605	24 November 2024

Result of Calibration

Gas	Reference Setting (mg/m ³)	Measured reading (mg/m ³)	Error (%)	Uncertainty (%)	Technical Requirement	Technical Reference Doc.
Dust - PM10	0.102	0.097	-5.0	17.0	± 10%	Mfr's Spec
Dust - PM10	0.198	0.194	-2.0	17.0	± 10%	Mfr's Spec
Dust - PM10	0.304	0.298	-2.0	17.0	± 10%	Mfr's Spec

CF-GAS-01

Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimate to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
 Note2: The standard by and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
 Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
 Note4: The result shown in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.
 Note5: Calibration item/ parameter marked with * is out of scope of Cal Lab Limited (92/A 3815/D1).

Calibrated By:

Wing Cheng
 Wing Cheng

Checked and Approved By:

Warren Yeung
 Warren Yeung

Company Chop:



Certificate Issue Date: 19 August 2024

CF-REG-04

*** End of Certificate ***

1. The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
 2. The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0022408
 Page 1 of 1

Personal Aerosol Monitor Performance check with High Volume Sampler

Performance Check ref. No. AS0240523-4 Report Issue Date 23/05/2024
 Date of performance check 23/05/2024

Objective:


A dust meter and a Total Suspended Particulate High Volume Air Sampler (HVS) were placed together to measure the Total Suspended Particulate (TSP) concentrations simultaneously to check the performance.

Equipment Used:

Equipment	Manufacturer and Model	Serial Number
Personal Aerosol Monitor	TSI AM510 Sidepak	11506014
Total Suspended Particulate High Volume Air Sampler	GS2310	10346

Result:

Equipment	Measurement Result, µg/m ³			
TSI AM510 Sidepak	72	153	264	357
High Volume Air Sampler (HVS)	41	116	181	267

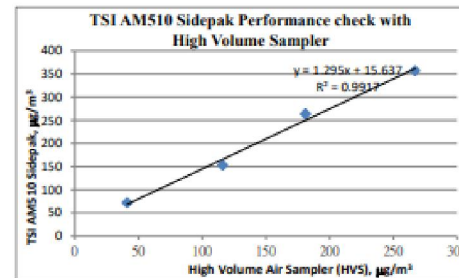

Tested by: (Poon Tsz Wing)
 Name: (Poon Tsz Wing)

Checked by: (Choy Ching Yee)
 Name: (Choy Ching Yee)

Form No. ENV-CAL-SAMPLER-CU1-01(2013-2001)

Catalogue of Weather Station

Cabled Vantage Pro2™ & Vantage Pro2 Plus™ Stations



**6152C
6162C**
Vantage Pro2™

The Vantage Pro2™ (# 6152C) and Vantage Pro2™ Plus (# 6162C) cabled weather stations include two components: the Integrated Sensor Suite (ISS) and the console. The ISS contains the sensor interface module (SIM), rain collector, an anemometer, and a passive radiation shield. The Vantage Pro2 console provides the user interface, data display, and calculations. The Vantage Pro2 Plus weather station includes two additional sensors that are optional on the Vantage Pro2 and purchased separately: the UV Sensor and the Solar Radiation Sensor. The console and ISS are powered by an AC-power adapter connected to the console. Batteries can be installed in the console to provide a backup power supply. Use WeatherLink™ to let your weather station interface with a computer, log data, and upload weather information to the Internet. The 6152C and 6162C models rely on passive shielding to reduce solar-radiation induced temperature errors in the outside temperature sensor readings.

Integrated Sensor Suite (ISS)

Operating Temperature	-40° to +150°F (-40° to +65°C)
Non-operating Temperature	-40° to +158°F (-40° to +70°C)
Current Draw	5 mA (average) at 4 to 6 VDC for ISS only. 10 mA average for both console and ISS
Connectors, Sensor	Modular RJ-11
Cable Type	4-conductor, 26 AWG
Cable Length, Anemometer	40' (12 m) (included); 240' (73 m) (maximum recommended)

Note: Maximum displayable wind decreases as the length of cable increases. at 140' (42 m) of cable, the maximum wind speed displayed is 135 mph (60 m/s); at 240' (73 m), the maximum wind speed displayed is 100 mph (34 m/s).

Wind Speed Sensor	Solid state magnetic sensor
Wind Direction Sensor	Wind vane with potentiometer
Rain Collector Type	Tipping bucket, 0.01" per tip (0.2 mm with metric rain adapter), 33.2 in ² (214 cm ²) collection area
Temperature Sensor Type	PN Junction Silicon Diode
Relative Humidity Sensor Type	Film capacitor element
Housing Material	UV-resistant ABS, polypropylene
Sensor Inputs	
RF Filtering	RC low-pass filter on each signal line

ISS Dimensions(not including anemometer or bird spikes):

Vantage Pro2 with Standard Rad Shield	14.0" x 9.4" x 14.5" (356 mm x 239 mm x 368 mm)
Vantage Pro2 with Fan-Aspirated Rad Shield	20.8" x 9.4" x 16.0" (528 mm x 239 mm x 406 mm)
Vantage Pro2 Plus with Standard Rad Shield	14.3" x 9.7" x 14.5" (363 mm x 246 mm x 368 mm)
Vantage Pro2 Plus with Fan-Aspirated Rad Shield	21.1" x 9.7" x 16.0" (536 mm x 246 mm x 406 mm)

DAVIS **® Davis Instruments** 3465 Diablo Ave., Hayward, CA 94545-2778 USA
(510) 732-9229 • FAX (510) 670-0599 • sales@davisinstruments.com • www.davisinstruments.com

DS6152C, 6162C Rev. W 12/7/13
1

7
Vantage Pro2™

Ultra Violet (UV) Radiation Index (requires UV sensor)

Resolution and Units	0.1 Index
Range	0 to 16 Index
Accuracy	±5% of full scale (Reference: Yankee UVB-1 at UV index 10 (Extremely High))
Cosine Response	±4% FS (0° to 90° zenith angle)
Update Interval	50 seconds to 1 minute (5 minutes when dark)
Current Graph Data	Instant Reading and Hourly Average; Daily, Monthly High
Historical Graph Data	Hourly Average, Daily, Monthly Highs
Alarm	High Threshold from Instant Calculation

Wind

Wind Chill (Calculated)	
Resolution and Units	1°F or 1°C (user-selectable); °C is converted from °F and rounded to the nearest 1°C
Range	-110° to +135°F (-79° to +57°C)
Accuracy	±2°F (±1°C) (typical)
Update Interval	10 to 12 seconds
Source	United States National Weather Service (NWS)/NOAA
Equation Used	Osczevski (1995) (adopted by US NWS in 2001)
Variables Used	Instant Outside Temperature and 10-min. Avg. Wind Speed
Current Display Data	Instant Calculation
Current Graph Data	Instant Calculation; Hourly, Daily and Monthly Low
Historical Graph Data	Hourly, Daily and Monthly Lows
Alarm	Low Threshold from Instant Calculation

Wind Direction

Range	1 - 360°
Display Resolution	16 points (22.5°) on compass rose, 1° in numeric display
Accuracy	±3°
Update Interval	2.5 to 3 seconds
Current Graph Data	Instant Reading (user adjustable); 10-min. Dominant; Hourly, Daily, Monthly Dominant
Historical Graph Data	Past 6 10-min. Dominants on compass rose only; Hourly, Daily, Monthly Dominants

Wind Speed

Resolution and Units	1 mph, 1 km/h, 0.4 m/s, or 1 knot (user-selectable) Measured in mph; other units are converted from mph and rounded to nearest 1 km/hr, 0.1 m/s, or 1 knot.
Range	0 to 200 mph, 0 to 173 knots, 0 to 89 m/s, 0 to 322 km/h
Update Interval	Instant Reading; 2.5 to 3 seconds, 10-minute Average: 1 minute
Accuracy	±2 mph (2 kts, 3.2 km/h, 0.9 m/s) or ±5%, whichever is greater
Maximum Cable Length	540' (165 m) (Note that maximum wind speed reading decreases as length of cable from anemometer to ISS increases.)
Current Display Data	Instant
Current Graph Data	Instant Reading; 10-minute and Hourly Average; Hourly High; Daily, Monthly and Yearly High with Direction of High
Historical Graph Data	10-min. and Hourly Averages; Hourly Highs; Daily, Monthly and Yearly Highs with Direction of Highs
Alarms	High Thresholds from Instant Reading and 10-minute Average

Calibration Certificate of Weather Station



Cal Lab Limited 校正實驗室有限公司
 Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
 Tsuen Wan, NT, Hong Kong
 Tel: +852 25680106 Email: info@callab.com.hk
 Fax: +852 30116194 Website: www.callab.com.hk

1024

Calibration Certificate No.: CC0862407

Information provided by customer

Customer: Castco Testing Centre Limited
 Address: 33, On Kui Street, Fanling, N.T.

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.:
Weather Station	Davis	Vantage PRO 2	BD181101023	AAST-WS-04

Certificate Information

Date of Receipt:	18 July 2024	Calibration Condition:	24.4°C, 54%RH, 998hPa
Date of Calibration:	24 July 2024	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	JJF 1183-2007, JJF 1076-2020, SOP-116	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Platinum resistance thermometer	KPPRHT-A-1	KCI I-1095, KCI P-1095	9 November 2024
Humidity sensor	KPPRHT-A-1	KCI I-1095, KCI P-1095	9 November 2024
Hot Wire Anemometer	9535	T95351316004	11 August 2024

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
 Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
 Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
 Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.

Approved By:

Warren Yeung
 Warren Yeung

Company Chop:



Certificate Issue Date: 29 July 2024

CTREG-04

1. The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
 2. The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0862407
 Page 1 of 2



Cal Lab Limited 校正實驗室有限公司
 Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
 Tsuen Wan, NT, Hong Kong
 Tel: +852 25680106 Email: info@callab.com.hk
 Fax: +852 30116194 Website: www.callab.com.hk

Result of Calibration

Temperature

Reference reading (°C)	Reading (°C)	Error (°C)	Uncertainty (°C)
15.0	16	1	2
20.0	20	0	2
25.0	25	0	2
30.0	30	0	2

Relative Humidity

Reference reading (%RH)	Reading (%RH)	Error (%RH)	Uncertainty (%RH)
40.0	39	-1	2
50.0	50	0	2
70.0	71	1	2

Barometric Pressure

Reference reading (hPa)	Reading (hPa)	Error (hPa)	Uncertainty (hPa)
950.0	950.3	0.3	2.8
1000.0	999.7	-0.3	2.8
1050.0	1049.4	-0.6	2.8

Wind Speed

Reference reading (m/s)	Measured reading (m/s)	Error (%)	Uncertainty (%)
0.0	0.0	N/A	3.6
2.0	1.9	-5.0	3.6
5.0	4.8	-2.0	3.6
8.0	7.9	-1.3	3.6

Wind Direction

Reference reading	Measured reading	Error	Uncertainty
0°	0°	0°	5°
45°	45°	0°	5°
90°	90°	0°	5°
135°	135°	0°	5°
180°	180°	0°	5°
225°	225°	0°	5°
270°	270°	0°	5°
315°	315°	0°	5°

*** End of Certificate ***

1. The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited
 2. The certificate is issued subject to the latest Terms and Conditions, available at our web site

CC0862407
 Page 2 of 2

Appendix F – Weather information

General Information

Date	Absolute Daily Min Temperature (°C)	Absolute Daily Max Temperature (°C)	Total Rainfall (mm)	Mean Relative Humidity (%)
1/2/2024	17.2	21.9	1.7	86
2/2/2024	17.5	20.1	Trace	86
3/2/2024	13.1	17.8	0.1	74
4/2/2024	12.2	18.6	0	61
5/2/2024	13.6	18.5	0	65
6/2/2024	15.9	20.1	0	57
7/2/2024	12.7	17.7	0	63
8/2/2024	11.5	17.2	0	43
9/2/2024	11.8	17.4	0	46
10/2/2024	12.8	19.1	0	63
11/2/2024	15.2	19.9	Trace	71
12/2/2024	17.2	20.3	23.8	93
13/2/2024	16.9	19.6	Trace	79
14/2/2024	15.5	18.2	0.2	87
15/2/2024	16.7	22.3	Trace	83
16/2/2024	17.8	25.1	0	81
17/2/2024	17.3	21.9	0	70
18/2/2024	16.7	20.4	0	71
19/2/2024	16.1	18.7	0	75
20/2/2024	16.6	19.8	0	79
21/2/2024	16.3	19.4	Trace	82
22/2/2024	15.5	18.1	Trace	80
23/2/2024	15.4	18.8	Trace	73
24/2/2024	13.0	19.5	0	67
25/2/2024	14.4	19.6	Trace	70
26/2/2024	16.1	20.7	0.3	76
27/2/2024	16.1	22.2	0	76
28/2/2024	18.1	25.4	0	77

NOTE1: The above weather information was obtained from manned weather station of Hong Kong Observatory.

NOTE2: Trace means rainfall less than 0.12 mm

<https://www.hko.gov.hk/en/cis/dailyExtract.htm?y=2025&m=2>

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
1/2/2025	0:00	0.4	90	2/2/2025	0:00	0.9	90	3/2/2025	0:00	0.9	247.5	4/2/2025	0:00	0.4	22.5
1/2/2025	1:00	0.4	112.5	2/2/2025	1:00	1.8	135	3/2/2025	1:00	0.4	270	4/2/2025	1:00	0.4	112.5
1/2/2025	2:00	0.9	90	2/2/2025	2:00	0.9	90	3/2/2025	2:00	0.4	112.5	4/2/2025	2:00	0.9	135
1/2/2025	3:00	0.4	135	2/2/2025	3:00	1.8	67.5	3/2/2025	3:00	0.4	112.5	4/2/2025	3:00	1.8	90
1/2/2025	4:00	0.4	112.5	2/2/2025	4:00	1.8	90	3/2/2025	4:00	0.4	90	4/2/2025	4:00	0.1	337.5
1/2/2025	5:00	0.4	90	2/2/2025	5:00	2.2	225	3/2/2025	5:00	0.9	112.5	4/2/2025	5:00	1.8	90
1/2/2025	6:00	0.4	90	2/2/2025	6:00	2.7	247.5	3/2/2025	6:00	1.8	90	4/2/2025	6:00	0.4	22.5
1/2/2025	7:00	0.9	135	2/2/2025	7:00	2.2	247.5	3/2/2025	7:00	1.8	90	4/2/2025	7:00	0.4	67.5
1/2/2025	8:00	0.4	90	2/2/2025	8:00	1.3	112.5	3/2/2025	8:00	2.2	90	4/2/2025	8:00	0.4	112.5
1/2/2025	9:00	1.3	135	2/2/2025	9:00	1.8	45	3/2/2025	9:00	2.7	90	4/2/2025	9:00	0.9	135
1/2/2025	10:00	1.8	90	2/2/2025	10:00	1.8	135	3/2/2025	10:00	2.2	112.5	4/2/2025	10:00	1.8	90
1/2/2025	11:00	1.3	90	2/2/2025	11:00	1.8	112.5	3/2/2025	11:00	1.3	157.5	4/2/2025	11:00	0.4	337.5
1/2/2025	12:00	1.3	202.5	2/2/2025	12:00	1.8	67.5	3/2/2025	12:00	1.8	90	4/2/2025	12:00	0.4	90
1/2/2025	13:00	1.3	112.5	2/2/2025	13:00	0.4	135	3/2/2025	13:00	1.8	67.5	4/2/2025	13:00	0.9	22.5
1/2/2025	14:00	1.8	90	2/2/2025	14:00	1.3	135	3/2/2025	14:00	1.8	45	4/2/2025	14:00	0.4	67.5
1/2/2025	15:00	1.3	112.5	2/2/2025	15:00	0.9	135	3/2/2025	15:00	1.8	22.5	4/2/2025	15:00	0.9	45
1/2/2025	16:00	0.9	112.5	2/2/2025	16:00	0.4	135	3/2/2025	16:00	0.4	67.5	4/2/2025	16:00	0.9	112.5
1/2/2025	17:00	0.9	112.5	2/2/2025	17:00	0.9	112.5	3/2/2025	17:00	1.3	292.5	4/2/2025	17:00	1.3	22.5
1/2/2025	18:00	0.9	112.5	2/2/2025	18:00	0.9	112.5	3/2/2025	18:00	0.9	112.5	4/2/2025	18:00	1.3	112.5
1/2/2025	19:00	0.4	90	2/2/2025	19:00	1.8	135	3/2/2025	19:00	0.4	135	4/2/2025	19:00	1.3	90
1/2/2025	20:00	0.9	90	2/2/2025	20:00	0.9	112.5	3/2/2025	20:00	0.4	112.5	4/2/2025	20:00	1.3	45
1/2/2025	21:00	0.9	112.5	2/2/2025	21:00	1.8	157.5	3/2/2025	21:00	0.9	135	4/2/2025	21:00	1.3	45
1/2/2025	22:00	0.4	112.5	2/2/2025	22:00	1.3	90	3/2/2025	22:00	1.3	112.5	4/2/2025	22:00	1.3	292.5
1/2/2025	23:00	0.4	112.5	2/2/2025	23:00	1.8	135	3/2/2025	23:00	1.8	90	4/2/2025	23:00	1.3	180

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
5/2/2025	0:00	0.4	135	6/2/2025	0:00	1.3	90	7/2/2025	0:00	1.3	135	8/2/2025	0:00	0.9	112.5
5/2/2025	1:00	0.9	90	6/2/2025	1:00	0.9	135	7/2/2025	1:00	0.9	90	8/2/2025	1:00	0.4	112.5
5/2/2025	2:00	0.9	112.5	6/2/2025	2:00	0.4	90	7/2/2025	2:00	0.9	90	8/2/2025	2:00	0.9	112.5
5/2/2025	3:00	0.9	202.5	6/2/2025	3:00	0.9	112.5	7/2/2025	3:00	0.9	22.5	8/2/2025	3:00	1.8	112.5
5/2/2025	4:00	1.3	67.5	6/2/2025	4:00	0.4	112.5	7/2/2025	4:00	0.9	90	8/2/2025	4:00	0.4	135
5/2/2025	5:00	1.3	67.5	6/2/2025	5:00	0.4	112.5	7/2/2025	5:00	0.9	45	8/2/2025	5:00	0.9	90
5/2/2025	6:00	0.9	45	6/2/2025	6:00	0.4	112.5	7/2/2025	6:00	1.3	90	8/2/2025	6:00	0.9	135
5/2/2025	7:00	1.3	112.5	6/2/2025	7:00	0.9	112.5	7/2/2025	7:00	1.3	90	8/2/2025	7:00	1.3	135
5/2/2025	8:00	1.8	315	6/2/2025	8:00	0.4	90	7/2/2025	8:00	0.9	22.5	8/2/2025	8:00	1.3	90
5/2/2025	9:00	1.8	135	6/2/2025	9:00	0.4	90	7/2/2025	9:00	1.3	315	8/2/2025	9:00	1.3	90
5/2/2025	10:00	0.9	292.5	6/2/2025	10:00	0.4	112.5	7/2/2025	10:00	1.8	45	8/2/2025	10:00	0.9	315
5/2/2025	11:00	0.9	135	6/2/2025	11:00	0.9	112.5	7/2/2025	11:00	1.8	22.5	8/2/2025	11:00	1.3	112.5
5/2/2025	12:00	1.3	45	6/2/2025	12:00	0.9	112.5	7/2/2025	12:00	0.9	292.5	8/2/2025	12:00	0.9	135
5/2/2025	13:00	1.8	315	6/2/2025	13:00	0.9	112.5	7/2/2025	13:00	0.9	67.5	8/2/2025	13:00	0.4	202.5
5/2/2025	14:00	1.8	22.5	6/2/2025	14:00	0.9	112.5	7/2/2025	14:00	0.4	22.5	8/2/2025	14:00	0.4	135
5/2/2025	15:00	0.4	112.5	6/2/2025	15:00	0.9	90	7/2/2025	15:00	0.9	45	8/2/2025	15:00	0.9	112.5
5/2/2025	16:00	0.9	45	6/2/2025	16:00	0.4	90	7/2/2025	16:00	0.9	45	8/2/2025	16:00	0.4	112.5
5/2/2025	17:00	0.4	112.5	6/2/2025	17:00	0.9	112.5	7/2/2025	17:00	0.4	67.5	8/2/2025	17:00	0.4	135
5/2/2025	18:00	0	45	6/2/2025	18:00	0.4	112.5	7/2/2025	18:00	0.9	135	8/2/2025	18:00	0.4	157.5
5/2/2025	19:00	0.4	67.5	6/2/2025	19:00	0.9	112.5	7/2/2025	19:00	0.9	135	8/2/2025	19:00	0.4	135
5/2/2025	20:00	0	202.5	6/2/2025	20:00	1.3	135	7/2/2025	20:00	0.9	135	8/2/2025	20:00	1.3	202.5
5/2/2025	21:00	0.4	247.5	6/2/2025	21:00	0.9	67.5	7/2/2025	21:00	0.9	112.5	8/2/2025	21:00	1.3	247.5
5/2/2025	22:00	0.4	135	6/2/2025	22:00	1.3	67.5	7/2/2025	22:00	1.3	45	8/2/2025	22:00	0.9	247.5
5/2/2025	23:00	1.8	67.5	6/2/2025	23:00	0.9	225	7/2/2025	23:00	1.3	180	8/2/2025	23:00	0.9	247.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
9/2/2025	0:00	0.4	90	10/2/2025	0:00	0.9	112.5	11/2/2025	0:00	0.4	202.5	12/2/2025	0:00	0.4	270
9/2/2025	1:00	0.4	112.5	10/2/2025	1:00	1.3	270	11/2/2025	1:00	0.4	247.5	12/2/2025	1:00	0.9	270
9/2/2025	2:00	0.9	135	10/2/2025	2:00	1.3	45	11/2/2025	2:00	0.4	247.5	12/2/2025	2:00	1.3	225
9/2/2025	3:00	1.3	45	10/2/2025	3:00	0.9	22.5	11/2/2025	3:00	0.4	247.5	12/2/2025	3:00	0.9	225
9/2/2025	4:00	0.9	112.5	10/2/2025	4:00	1.3	45	11/2/2025	4:00	0.4	90	12/2/2025	4:00	0.9	225
9/2/2025	5:00	0.9	90	10/2/2025	5:00	0.9	22.5	11/2/2025	5:00	0.9	90	12/2/2025	5:00	0.9	315
9/2/2025	6:00	0.9	22.5	10/2/2025	6:00	0.4	22.5	11/2/2025	6:00	0.9	22.5	12/2/2025	6:00	0.9	315
9/2/2025	7:00	0.9	90	10/2/2025	7:00	0.4	22.5	11/2/2025	7:00	0.9	90	12/2/2025	7:00	0.9	315
9/2/2025	8:00	0.9	45	10/2/2025	8:00	0.9	22.5	11/2/2025	8:00	0.9	247.5	12/2/2025	8:00	0.4	157.5
9/2/2025	9:00	0.4	90	10/2/2025	9:00	1.3	22.5	11/2/2025	9:00	0.4	112.5	12/2/2025	9:00	0.4	157.5
9/2/2025	10:00	0.4	90	10/2/2025	10:00	0.9	22.5	11/2/2025	10:00	0.4	157.5	12/2/2025	10:00	0.4	202.5
9/2/2025	11:00	0.4	112.5	10/2/2025	11:00	0.9	22.5	11/2/2025	11:00	0.4	202.5	12/2/2025	11:00	0.4	202.5
9/2/2025	12:00	0.9	45	10/2/2025	12:00	0.9	22.5	11/2/2025	12:00	0.4	112.5	12/2/2025	12:00	1.3	270
9/2/2025	13:00	0.4	67.5	10/2/2025	13:00	0.9	45	11/2/2025	13:00	0.4	247.5	12/2/2025	13:00	1.3	315
9/2/2025	14:00	0.9	135	10/2/2025	14:00	0.9	90	11/2/2025	14:00	0.4	270	12/2/2025	14:00	0.9	315
9/2/2025	15:00	0.9	135	10/2/2025	15:00	0.4	90	11/2/2025	15:00	0.4	247.5	12/2/2025	15:00	0.9	315
9/2/2025	16:00	0.9	135	10/2/2025	16:00	0.4	22.5	11/2/2025	16:00	0.4	247.5	12/2/2025	16:00	1.3	157.5
9/2/2025	17:00	0.9	112.5	10/2/2025	17:00	0.4	315	11/2/2025	17:00	0.4	247.5	12/2/2025	17:00	1.8	157.5
9/2/2025	18:00	1.3	45	10/2/2025	18:00	0.4	45	11/2/2025	18:00	0.4	67.5	12/2/2025	18:00	1.8	202.5
9/2/2025	19:00	1.3	180	10/2/2025	19:00	0.9	22.5	11/2/2025	19:00	0.4	112.5	12/2/2025	19:00	1.3	202.5
9/2/2025	20:00	1.3	180	10/2/2025	20:00	0.9	292.5	11/2/2025	20:00	0.4	270	12/2/2025	20:00	1.8	270
9/2/2025	21:00	0.9	180	10/2/2025	21:00	0.9	67.5	11/2/2025	21:00	0.4	315	12/2/2025	21:00	1.8	270
9/2/2025	22:00	0.9	180	10/2/2025	22:00	0.9	112.5	11/2/2025	22:00	0.9	270	12/2/2025	22:00	0.9	247.5
9/2/2025	23:00	0.4	22.5	10/2/2025	23:00	0.4	225	11/2/2025	23:00	1.3	270	12/2/2025	23:00	0.9	135

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
13/2/2025	0:00	3.1	247.5	14/2/2025	0:00	0.4	247.5	15/2/2025	0:00	5	45	16/2/2025	0:00	3.6	67.5
13/2/2025	1:00	4	90	14/2/2025	1:00	4.5	90	15/2/2025	1:00	3.6	90	16/2/2025	1:00	4.5	292.5
13/2/2025	2:00	5.8	90	14/2/2025	2:00	4.5	112.5	15/2/2025	2:00	3.6	90	16/2/2025	2:00	3.6	112.5
13/2/2025	3:00	4.5	90	14/2/2025	3:00	4.9	112.5	15/2/2025	3:00	4.5	90	16/2/2025	3:00	4.5	135
13/2/2025	4:00	4.9	90	14/2/2025	4:00	5.4	135	15/2/2025	4:00	3.6	90	16/2/2025	4:00	3.6	135
13/2/2025	5:00	4	135	14/2/2025	5:00	4	135	15/2/2025	5:00	4.5	135	16/2/2025	5:00	3.6	135
13/2/2025	6:00	5.1	315	14/2/2025	6:00	5	67.5	15/2/2025	6:00	3.6	315	16/2/2025	6:00	4	315
13/2/2025	7:00	5.1	112.5	14/2/2025	7:00	3.6	22.5	15/2/2025	7:00	3.6	112.5	16/2/2025	7:00	4	112.5
13/2/2025	8:00	5.1	337.5	14/2/2025	8:00	3.6	135	15/2/2025	8:00	4	337.5	16/2/2025	8:00	3.6	135
13/2/2025	9:00	4	270	14/2/2025	9:00	4.5	180	15/2/2025	9:00	4	270	16/2/2025	9:00	3.6	45
13/2/2025	10:00	5.8	315	14/2/2025	10:00	3.6	337.5	15/2/2025	10:00	3.6	315	16/2/2025	10:00	4.5	90
13/2/2025	11:00	4.5	45	14/2/2025	11:00	4.5	22.5	15/2/2025	11:00	3.6	45	16/2/2025	11:00	3.6	292.5
13/2/2025	12:00	5.8	337.5	14/2/2025	12:00	3.6	292.5	15/2/2025	12:00	4.5	135	16/2/2025	12:00	4.5	112.5
13/2/2025	13:00	4.9	270	14/2/2025	13:00	3.6	270	15/2/2025	13:00	3.6	67.5	16/2/2025	13:00	3.6	135
13/2/2025	14:00	4.5	45	14/2/2025	14:00	5.8	270	15/2/2025	14:00	4.5	22.5	16/2/2025	14:00	3.6	135
13/2/2025	15:00	4.5	45	14/2/2025	15:00	6.3	90	15/2/2025	15:00	3.6	135	16/2/2025	15:00	5.8	135
13/2/2025	16:00	4.9	112.5	14/2/2025	16:00	6.3	112.5	15/2/2025	16:00	3.6	180	16/2/2025	16:00	3.6	315
13/2/2025	17:00	5.4	90	14/2/2025	17:00	5.4	270	15/2/2025	17:00	5.8	337.5	16/2/2025	17:00	3.6	112.5
13/2/2025	18:00	4	112.5	14/2/2025	18:00	4.5	112.5	15/2/2025	18:00	6.3	22.5	16/2/2025	18:00	4.5	135
13/2/2025	19:00	5	90	14/2/2025	19:00	4.8	135	15/2/2025	19:00	6.3	292.5	16/2/2025	19:00	3.6	45
13/2/2025	20:00	3.6	90	14/2/2025	20:00	4.5	45	15/2/2025	20:00	5.4	270	16/2/2025	20:00	1.8	90
13/2/2025	21:00	3.6	90	14/2/2025	21:00	5.4	225	15/2/2025	21:00	4.5	270	16/2/2025	21:00	1.8	135
13/2/2025	22:00	4.5	90	14/2/2025	22:00	4.5	225	15/2/2025	22:00	4.8	90	16/2/2025	22:00	1.3	112.5
13/2/2025	23:00	4	112.5	14/2/2025	23:00	4.5	112.5	15/2/2025	23:00	4.5	112.5	16/2/2025	23:00	1.3	247.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
17/2/2025	0:00	1.3	112.5	18/2/2025	0:00	1.3	112.5	19/2/2025	0:00	1.3	112.5	20/2/2025	0:00	1.3	67.5
17/2/2025	1:00	0.9	45	18/2/2025	1:00	1.8	112.5	19/2/2025	1:00	1.3	157.5	20/2/2025	1:00	0.4	45
17/2/2025	2:00	1.3	90	18/2/2025	2:00	1.8	135	19/2/2025	2:00	1.8	135	20/2/2025	2:00	1.3	112.5
17/2/2025	3:00	0.9	247.5	18/2/2025	3:00	2.2	112.5	19/2/2025	3:00	2.2	112.5	20/2/2025	3:00	0.9	157.5
17/2/2025	4:00	0.9	112.5	18/2/2025	4:00	2.2	67.5	19/2/2025	4:00	2.2	135	20/2/2025	4:00	1.3	135
17/2/2025	5:00	0.4	112.5	18/2/2025	5:00	2.2	90	19/2/2025	5:00	3	112.5	20/2/2025	5:00	0.9	112.5
17/2/2025	6:00	1.8	112.5	18/2/2025	6:00	1.8	337.5	19/2/2025	6:00	2.7	112.5	20/2/2025	6:00	0.4	135
17/2/2025	7:00	1.8	135	18/2/2025	7:00	1.8	22.5	19/2/2025	7:00	4.9	90	20/2/2025	7:00	0.9	112.5
17/2/2025	8:00	2.2	90	18/2/2025	8:00	1.3	315	19/2/2025	8:00	4.5	135	20/2/2025	8:00	0.4	112.5
17/2/2025	9:00	2.7	337.5	18/2/2025	9:00	1.3	112.5	19/2/2025	9:00	4.5	112.5	20/2/2025	9:00	1.3	90
17/2/2025	10:00	2.2	90	18/2/2025	10:00	1.3	112.5	19/2/2025	10:00	3.6	292.5	20/2/2025	10:00	1.8	135
17/2/2025	11:00	1.3	22.5	18/2/2025	11:00	0.4	112.5	19/2/2025	11:00	4.5	292.5	20/2/2025	11:00	0.9	112.5
17/2/2025	12:00	0.9	112.5	18/2/2025	12:00	0.4	90	19/2/2025	12:00	2.2	315	20/2/2025	12:00	0.9	292.5
17/2/2025	13:00	0.9	247.5	18/2/2025	13:00	0.4	22.5	19/2/2025	13:00	1.3	112.5	20/2/2025	13:00	0.4	292.5
17/2/2025	14:00	0.9	112.5	18/2/2025	14:00	0.9	45	19/2/2025	14:00	1.8	135	20/2/2025	14:00	0.4	315
17/2/2025	15:00	0.4	112.5	18/2/2025	15:00	0.9	135	19/2/2025	15:00	1.3	90	20/2/2025	15:00	0.4	112.5
17/2/2025	16:00	1.8	112.5	18/2/2025	16:00	0.4	315	19/2/2025	16:00	1.3	22.5	20/2/2025	16:00	0.4	90
17/2/2025	17:00	1.8	135	18/2/2025	17:00	0.9	112.5	19/2/2025	17:00	1.3	135	20/2/2025	17:00	0.4	90
17/2/2025	18:00	2.2	90	18/2/2025	18:00	0.9	112.5	19/2/2025	18:00	1.3	135	20/2/2025	18:00	0.4	90
17/2/2025	19:00	2.7	337.5	18/2/2025	19:00	0.4	90	19/2/2025	19:00	1.3	90	20/2/2025	19:00	0.4	67.5
17/2/2025	20:00	2.2	90	18/2/2025	20:00	0.4	135	19/2/2025	20:00	0.9	45	20/2/2025	20:00	0.9	90
17/2/2025	21:00	1.3	22.5	18/2/2025	21:00	0.9	90	19/2/2025	21:00	0.4	22.5	20/2/2025	21:00	0.9	135
17/2/2025	22:00	0.9	112.5	18/2/2025	22:00	0.9	45	19/2/2025	22:00	0.9	45	20/2/2025	22:00	0.4	135
17/2/2025	23:00	1.3	67.5	18/2/2025	23:00	0.4	247.5	19/2/2025	23:00	0.9	135	20/2/2025	23:00	0.9	22.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
21/2/2025	0:00	0.4	45	22/2/2025	0:00	1.3	225	23/2/2025	0:00	0.4	315	24/2/2025	0:00	0.9	112.5
21/2/2025	1:00	0.9	90	22/2/2025	1:00	0.9	247.5	23/2/2025	1:00	0.9	112.5	24/2/2025	1:00	0.9	67.5
21/2/2025	2:00	0.4	112.5	22/2/2025	2:00	0.9	292.5	23/2/2025	2:00	0.9	112.5	24/2/2025	2:00	1.3	90
21/2/2025	3:00	0.4	202.5	22/2/2025	3:00	0.4	247.5	23/2/2025	3:00	0.4	90	24/2/2025	3:00	0.9	135
21/2/2025	4:00	0.4	45	22/2/2025	4:00	0.9	225	23/2/2025	4:00	0.9	135	24/2/2025	4:00	0.9	135
21/2/2025	5:00	0.9	337.5	22/2/2025	5:00	1.3	247.5	23/2/2025	5:00	0.9	90	24/2/2025	5:00	0.9	112.5
21/2/2025	6:00	1.3	135	22/2/2025	6:00	0.9	225	23/2/2025	6:00	0.9	45	24/2/2025	6:00	0.9	112.5
21/2/2025	7:00	1.3	112.5	22/2/2025	7:00	0.9	270	23/2/2025	7:00	1.3	22.5	24/2/2025	7:00	1.3	247.5
21/2/2025	8:00	1.3	22.5	22/2/2025	8:00	0.9	270	23/2/2025	8:00	1.8	45	24/2/2025	8:00	1.3	225
21/2/2025	9:00	1.3	45	22/2/2025	9:00	1.8	45	23/2/2025	9:00	1.3	135	24/2/2025	9:00	0.4	90
21/2/2025	10:00	1.3	315	22/2/2025	10:00	1.3	22.5	23/2/2025	10:00	1.3	315	24/2/2025	10:00	0.9	67.5
21/2/2025	11:00	0.4	45	22/2/2025	11:00	0.9	157.5	23/2/2025	11:00	1.3	112.5	24/2/2025	11:00	0.9	112.5
21/2/2025	12:00	0.4	45	22/2/2025	12:00	0.4	22.5	23/2/2025	12:00	0.4	67.5	24/2/2025	12:00	0.9	45
21/2/2025	13:00	3.1	337.5	22/2/2025	13:00	0.9	112.5	23/2/2025	13:00	0.9	112.5	24/2/2025	13:00	0.9	90
21/2/2025	14:00	2.7	157.5	22/2/2025	14:00	0.4	67.5	23/2/2025	14:00	0.9	202.5	24/2/2025	14:00	0.9	90
21/2/2025	15:00	0.1	202.5	22/2/2025	15:00	0.4	67.5	23/2/2025	15:00	0.4	202.5	24/2/2025	15:00	1.3	112.5
21/2/2025	16:00	1.8	202.5	22/2/2025	16:00	0.4	67.5	23/2/2025	16:00	0.9	247.5	24/2/2025	16:00	0.9	112.5
21/2/2025	17:00	0.4	202.5	22/2/2025	17:00	0.4	135	23/2/2025	17:00	0.9	225	24/2/2025	17:00	1.8	112.5
21/2/2025	18:00	0.9	202.5	22/2/2025	18:00	0.9	67.5	23/2/2025	18:00	0.9	157.5	24/2/2025	18:00	2.2	135
21/2/2025	19:00	0.9	135	22/2/2025	19:00	0.9	90	23/2/2025	19:00	0.9	202.5	24/2/2025	19:00	2.2	135
21/2/2025	20:00	0.9	135	22/2/2025	20:00	0.4	112.5	23/2/2025	20:00	0.4	202.5	24/2/2025	20:00	1.8	135
21/2/2025	21:00	1.3	112.5	22/2/2025	21:00	0.9	112.5	23/2/2025	21:00	0.4	112.5	24/2/2025	21:00	1.8	135
21/2/2025	22:00	0.4	90	22/2/2025	22:00	1.3	90	23/2/2025	22:00	0.9	112.5	24/2/2025	22:00	0.4	67.5
21/2/2025	23:00	0.9	22.5	22/2/2025	23:00	0.4	67.5	23/2/2025	23:00	0.4	225	24/2/2025	23:00	0.4	45

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
25/2/2025	0:00	0.9	45	26/2/2025	0:00	1.3	90	27/2/2025	0:00	0.9	22.5	28/2/2025	0:00	1.8	135
25/2/2025	1:00	0.9	45	26/2/2025	1:00	1.3	112.5	27/2/2025	1:00	1.3	22.5	28/2/2025	1:00	1.8	270
25/2/2025	2:00	1.8	45	26/2/2025	2:00	1.3	135	27/2/2025	2:00	0.9	180	28/2/2025	2:00	0.9	247.5
25/2/2025	3:00	1.3	45	26/2/2025	3:00	1.3	90	27/2/2025	3:00	0.9	90	28/2/2025	3:00	0.9	247.5
25/2/2025	4:00	1.3	112.5	26/2/2025	4:00	1.3	90	27/2/2025	4:00	0.4	135	28/2/2025	4:00	0.9	247.5
25/2/2025	5:00	1.3	90	26/2/2025	5:00	0.9	90	27/2/2025	5:00	0.4	202.5	28/2/2025	5:00	0	90
25/2/2025	6:00	1.3	90	26/2/2025	6:00	1.3	112.5	27/2/2025	6:00	0.9	112.5	28/2/2025	6:00	0.9	67.5
25/2/2025	7:00	1.3	112.5	26/2/2025	7:00	1.3	112.5	27/2/2025	7:00	0.9	135	28/2/2025	7:00	0.9	67.5
25/2/2025	8:00	0.9	67.5	26/2/2025	8:00	0.9	90	27/2/2025	8:00	1.3	112.5	28/2/2025	8:00	1.8	90
25/2/2025	9:00	1.3	67.5	26/2/2025	9:00	1.3	112.5	27/2/2025	9:00	1.3	112.5	28/2/2025	9:00	1.3	90
25/2/2025	10:00	1.3	112.5	26/2/2025	10:00	1.3	135	27/2/2025	10:00	1.3	90	28/2/2025	10:00	1.3	67.5
25/2/2025	11:00	0.9	112.5	26/2/2025	11:00	1.3	112.5	27/2/2025	11:00	1.8	22.5	28/2/2025	11:00	1.3	112.5
25/2/2025	12:00	1.3	112.5	26/2/2025	12:00	1.3	90	27/2/2025	12:00	0.4	90	28/2/2025	12:00	1.3	90
25/2/2025	13:00	1.3	112.5	26/2/2025	13:00	1.3	135	27/2/2025	13:00	1.3	112.5	28/2/2025	13:00	1.3	112.5
25/2/2025	14:00	1.3	135	26/2/2025	14:00	1.3	112.5	27/2/2025	14:00	1.3	225	28/2/2025	14:00	0.9	90
25/2/2025	15:00	1.3	112.5	26/2/2025	15:00	0.9	112.5	27/2/2025	15:00	0.9	270	28/2/2025	15:00	1.3	90
25/2/2025	16:00	1.3	112.5	26/2/2025	16:00	1.3	112.5	27/2/2025	16:00	0.9	22.5	28/2/2025	16:00	1.3	112.5
25/2/2025	17:00	1.3	135	26/2/2025	17:00	1.3	112.5	27/2/2025	17:00	0.9	22.5	28/2/2025	17:00	0.9	90
25/2/2025	18:00	0.9	67.5	26/2/2025	18:00	0.4	135	27/2/2025	18:00	0.9	22.5	28/2/2025	18:00	1.3	135
25/2/2025	19:00	0.4	112.5	26/2/2025	19:00	0.9	135	27/2/2025	19:00	0.9	22.5	28/2/2025	19:00	1.3	180
25/2/2025	20:00	0.4	45	26/2/2025	20:00	0.9	90	27/2/2025	20:00	0.9	90	28/2/2025	20:00	1.3	180
25/2/2025	21:00	0.9	90	26/2/2025	21:00	0.9	135	27/2/2025	21:00	0.9	225	28/2/2025	21:00	1.3	157.5
25/2/2025	22:00	0.9	90	26/2/2025	22:00	0.9	112.5	27/2/2025	22:00	0.4	225	28/2/2025	22:00	1.3	157.5
25/2/2025	23:00	0.4	112.5	26/2/2025	23:00	0.4	112.5	27/2/2025	23:00	0.4	225	28/2/2025	23:00	1.3	157.5

Appendix G – 24-hr TSP monitoring results and graphical presentation



Location: AM2(A) – Ng Wah Catholic Secondary School

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
3/2/2025	Sunny	17.8	1019.6	18.0019	18.0467	0.0448	2025/2/3 13:05	2025/2/4 13:05	1440	52	52	1.50	2155	21
8/2/2025	Sunny	17.5	1024.6	18.0233	18.1714	0.1481	2025/2/8 9:05	2025/2/9 9:05	1440	50	50	1.44	2077	71
14/2/2025	Cloudy	16.3	1017.9	18.2189	18.2834	0.0645	2025/2/14 9:30	2025/2/15 9:30	1440	50	50	1.44	2075	31
20/2/2025	Sunny	18.6	1021.2	18.1225	18.1933	0.0708	2025/2/20 13:25	2025/2/21 13:25	1440	50	50	1.44	2070	34
26/2/2025	Cloudy	18.3	1022.9	15.5261	15.6673	0.1412	2025/2/26 9:15	2025/2/27 9:15	1440	52	52	1.50	2156	65
													Maximum	71
													Minimum	21
													Average	44
													Action Level	175
													Limit Level	260

Location: AM3 – Sky Tower

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
3/2/2025	Sunny	17.8	1019.6	15.0063	15.0802	0.0739	2025/2/3 9:34	2025/2/4 9:34	1440	52	52	1.48	2137	35
8/2/2025	Sunny	17.5	1024.6	18.2632	18.4144	0.1512	2025/2/8 13:23	2025/2/9 13:23	1440	50	50	1.43	2060	73
14/2/2025	Cloudy	16.3	1017.9	18.4311	18.5272	0.0961	2025/2/14 13:36	2025/2/15 13:36	1440	50	50	1.43	2058	47
20/2/2025	Sunny	18.6	1021.2	18.3206	18.4425	0.1219	2025/2/20 9:41	2025/2/21 9:41	1440	50	50	1.43	2053	59
26/2/2025	Cloudy	18.3	1022.9	15.0575	15.2528	0.1953	2025/2/26 13:39	2025/2/27 13:39	1440	50	50	1.43	2056	95
												Maximum	95	
												Minimum	35	
												Average	62	
												Action Level	172	
												Limit Level	260	

24-hour average TSP

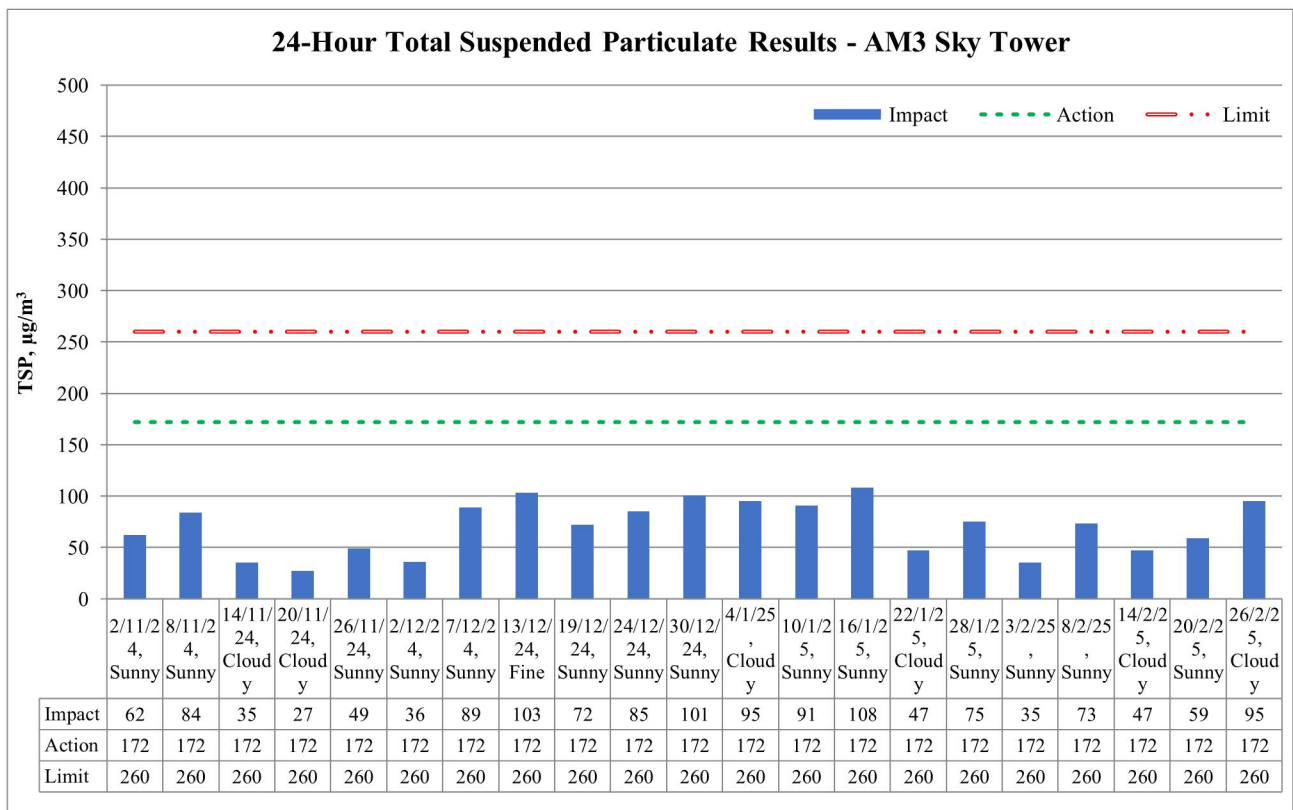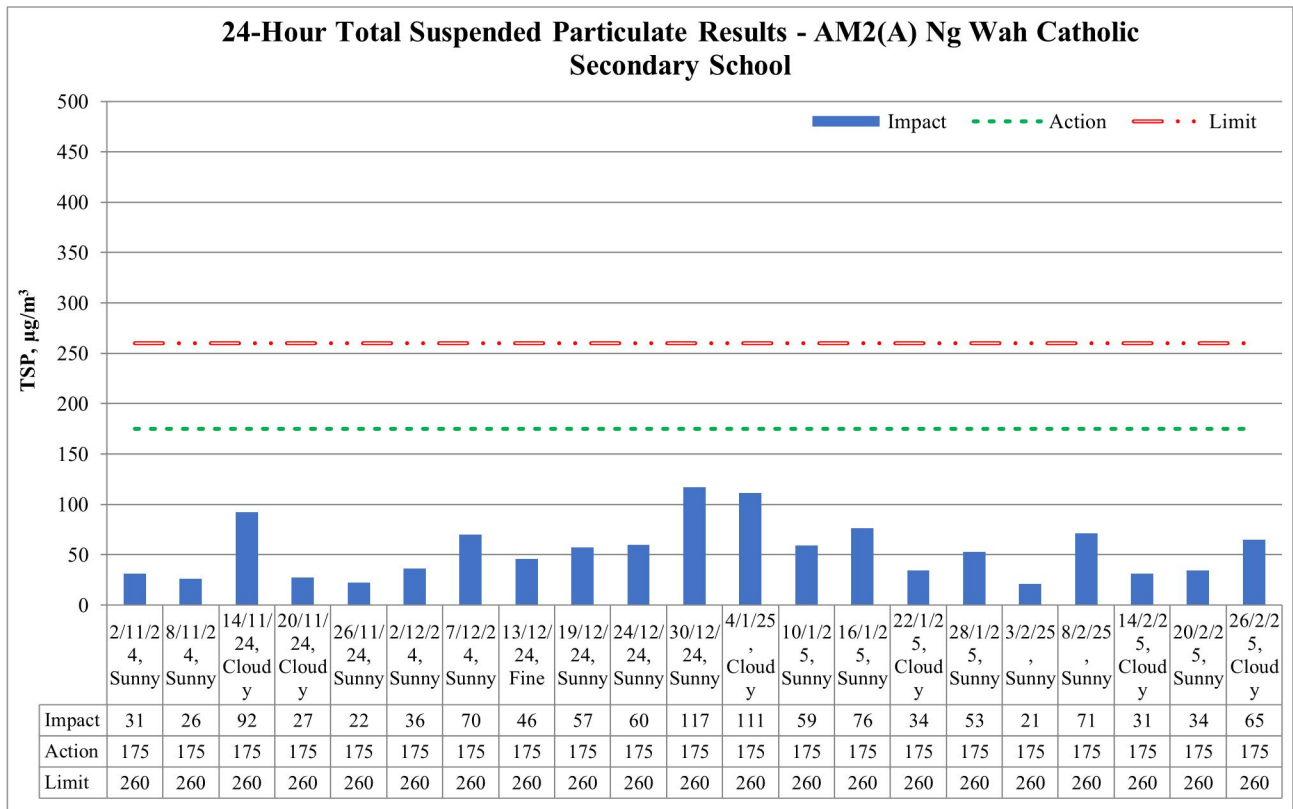

Major Construction Activities	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Floor screeding works at deck level of LW-02	✓	✓		
Backfilling at retaining wall for S14	✓	✓		
Construction works for DCS	✓	✓	✓	✓
Construction of LW02 structural steel roof	✓	✓		
Construction of Parapet for S14	✓	✓	✓	✓
Construction of bridge deck of S14	✓	✓	✓	
Construction of headwall at Subway SB01 Retrieval Shaft	✓	✓	✓	✓
Drainage construction and backfilling works for retaining wall of S14	✓			
Drainage construction works at PS2 and PS3	✓	✓	✓	✓
Renovation works for Subway KS10 Lift and Staircase	✓	✓	✓	✓
Renovation works for existing subways KS10	✓			
Road and Drain Construction works for Road L16, Commercial Street and Road D1	✓	✓	✓	✓
Tiling works at LW02	✓	✓	✓	✓
Tiling works at LW-02 and Subway KS10	✓	✓		
Lift installation at LW-02 and KS10	✓	✓		
Installation of glass panel and aluminum panels of LW02	✓	✓	✓	✓
Installation of glass balustrade at LW02	✓			
Installation of drainage system of pump house for KS10	✓	✓		
Ceiling painting and plastering inside Subway SB-01	✓	✓	✓	✓
Installation of VE panel sub-frame in Subway SB-01	✓			
Lift installation at LW02 and KS10	✓	✓	✓	✓
Demolition of existing parapet of K73	✓	✓	✓	✓
SB01 Sa Po Rd Retrieval Shaft Headwall RC construction	✓	✓	✓	✓
Installation of lighting system at LW-02		✓	✓	✓
Refurbishment for Bridge K73		✓	✓	✓
Drainage construction of S14		✓	✓	✓
Dismantling of portal frame at Bridge K73		✓		
Installation of steel formwork for curved top slab of headwall at Retrieval Shaft of Subway SB-01		✓	✓	
Watermain and road works at PS3		✓	✓	✓
Installation of cable tray at LW-02			✓	✓
Installation of glass balustrade at bridge deck of LW02			✓	✓
Installation of geotextile and subsoil drainage for planters at LW02			✓	✓
Installation of movement joint for S14			✓	✓
Installation of canopy at LW-02				✓
Asphalt application at S14			✓	✓

Factors might affect the monitoring results	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Non-project related construction activities in the adjacent construction sites were observed.	✓	✓	✓	✓

Appendix H – 1-hr TSP monitoring results and graphical presentation


Location:
**AM2(A) –
 Ng Wah Catholic
 Secondary School**

Date	Measurement Period			1-hr TSP concentration, $\mu\text{g}/\text{m}^3$	Weather
		-			
03/02/2025	13:00	-	14:00	35	Sunny
	14:00	-	15:00	37	
	15:00	-	16:00	36	
08/02/2025	9:00	-	10:00	65	Sunny
	10:00	-	11:00	77	
	11:00	-	12:00	76	
14/02/2025	9:00	-	10:00	44	Cloudy
	10:00	-	11:00	45	
	11:00	-	12:00	58	
20/02/2025	13:00	-	14:00	40	Sunny
	14:00	-	15:00	45	
	15:00	-	16:00	42	
26/02/2025	9:00	-	10:00	65	Cloudy
	10:00	-	11:00	68	
	11:00	-	12:00	70	
Maximum				77	
Minimum				35	
Average				54	
Action Level				302	
Limit Level				500	


Location:
**AM3 -
 Sky Tower**

Date	Measurement Period			1-hr TSP concentration, μg/m ³	Weather
03/02/2025	9:00	-	10:00	34	Sunny
	10:00	-	11:00	37	
	11:00	-	12:00	37	
08/02/2025	13:00	-	14:00	67	Sunny
	14:00	-	15:00	70	
	15:00	-	16:00	68	
14/02/2025	13:00	-	14:00	40	Cloudy
	14:00	-	15:00	45	
	15:00	-	16:00	46	
20/02/2025	9:00	-	10:00	49	Sunny
	10:00	-	11:00	51	
	11:00	-	12:00	53	
26/02/2025	13:00	-	14:00	72	Cloudy
	14:00	-	15:00	72	
	15:00	-	16:00	78	
Maximum				78	
Minimum				34	
Average				55	
Action Level				301	
Limit Level				500	

1-hour average TSP

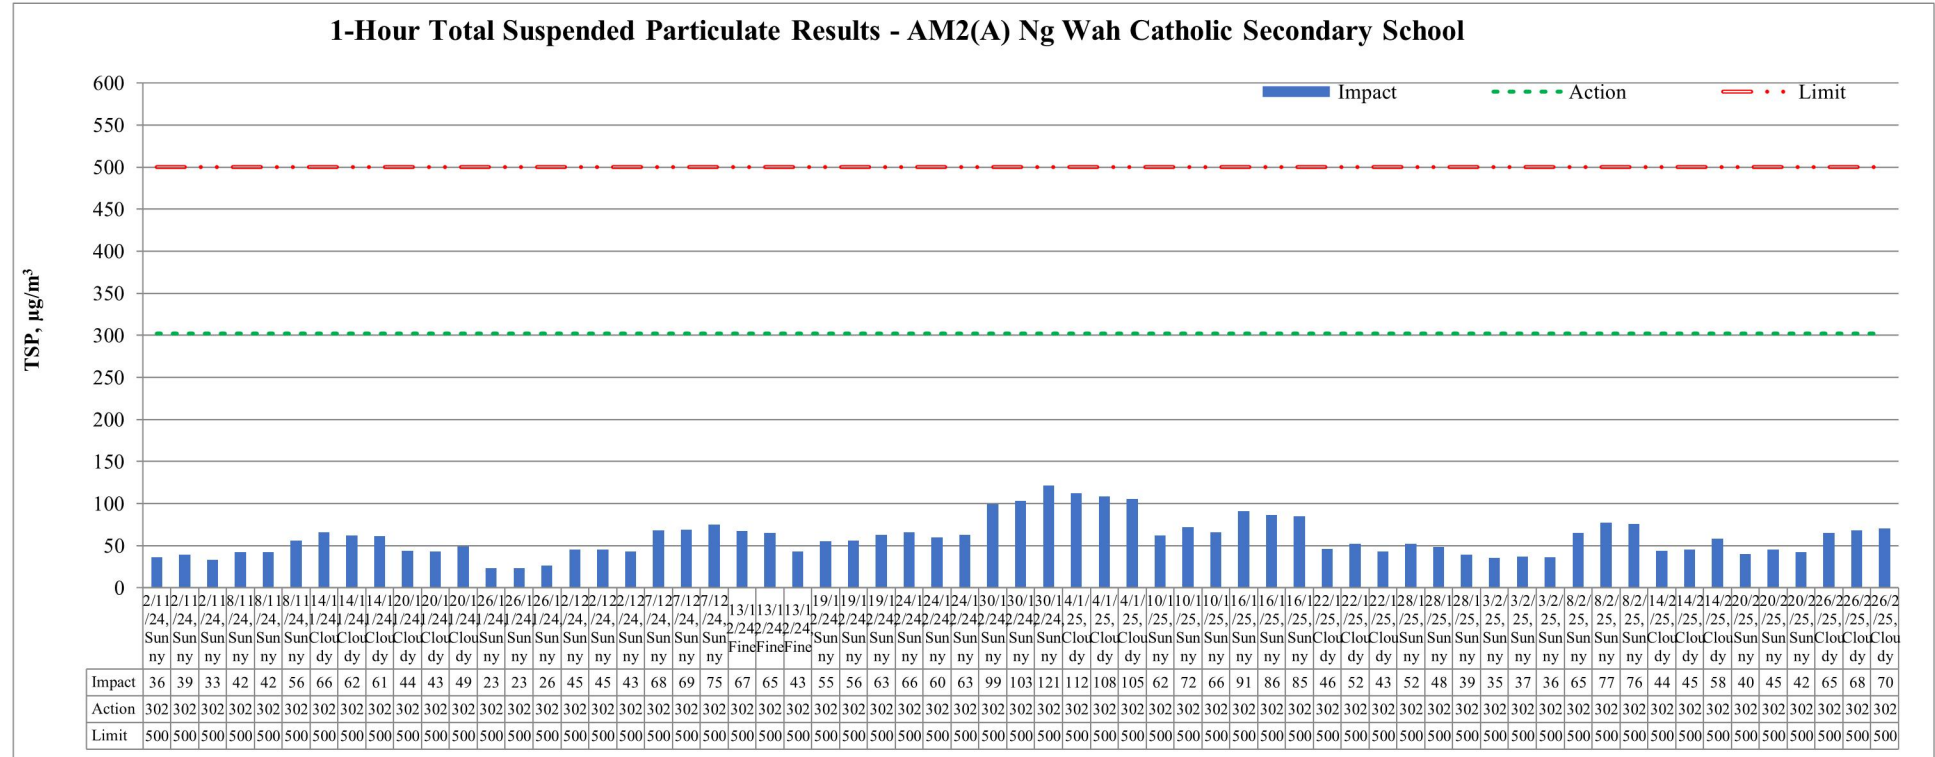

1-Hour Total Suspended Particulate Results - AM3 Sky Tower

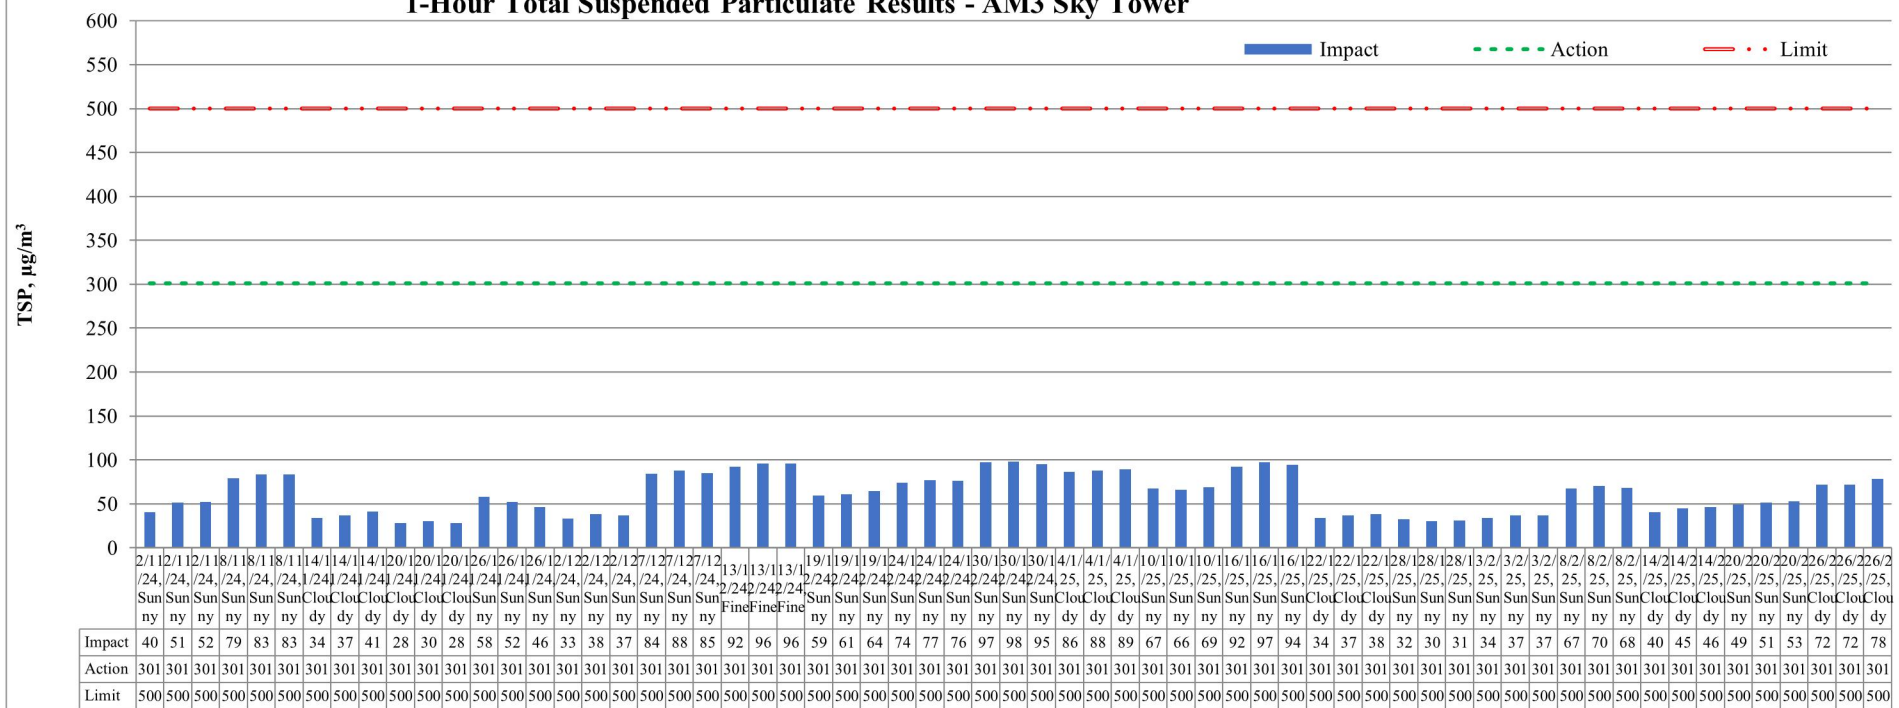

Major Construction Activities	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Floor screeding works at deck level of LW-02	✓	✓		
Backfilling at retaining wall for S14	✓	✓		
Construction works for DCS	✓	✓	✓	✓
Construction of LW02 structural steel roof	✓	✓		
Construction of Parapet for S14	✓	✓	✓	✓
Construction of bridge deck of S14	✓	✓	✓	
Construction of headwall at Subway SB01 Retrieval Shaft	✓	✓	✓	✓
Drainage construction and backfilling works for retaining wall of S14	✓			
Drainage construction works at PS2 and PS3	✓	✓	✓	✓
Renovation works for Subway KS10 Lift and Staircase	✓	✓	✓	✓
Renovation works for existing subways KS10	✓			
Road and Drain Construction works for Road L16, Commercial Street and Road D1	✓	✓	✓	✓
Tiling works at LW02	✓	✓	✓	✓
Tiling works at LW-02 and Subway KS10	✓	✓		
Lift installation at LW-02 and KS10	✓	✓		
Installation of glass panel and aluminum panels of LW02	✓	✓	✓	✓
Installation of glass balustrade at LW02	✓			
Installation of drainage system of pump house for KS10	✓	✓		
Ceiling painting and plastering inside Subway SB-01	✓	✓	✓	✓
Installation of VE panel sub-frame in Subway SB-01	✓			
Lift installation at LW02 and KS10	✓	✓	✓	✓
Demolition of existing parapet of K73	✓	✓	✓	✓
SB01 Sa Po Rd Retrieval Shaft Headwall RC construction	✓	✓	✓	✓
Installation of lighting system at LW-02		✓	✓	✓
Refurbishment for Bridge K73		✓	✓	✓
Drainage construction of S14		✓	✓	✓
Dismantling of portal frame at Bridge K73		✓		
Installation of steel formwork for curved top slab of headwall at Retrieval Shaft of Subway SB-01		✓	✓	
Watermain and road works at PS3		✓	✓	✓
Installation of cable tray at LW-02			✓	✓
Installation of glass balustrade at bridge deck of LW02			✓	✓
Installation of geotextile and subsoil drainage for planters at LW02			✓	✓
Installation of movement joint for S14			✓	✓
Installation of canopy at LW-02				✓
Asphalt application at S14			✓	✓

Factors might affect the monitoring results	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Non-project related construction activities in the adjacent construction sites were observed.	✓	✓	✓	✓

Appendix I – Event and Action Plan for air quality


Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC and Supervisor /ER; 3. Repeat measurement to confirm finding. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC and Supervisor /ER; 3. Increase monitoring frequency to daily; 4. Discuss with IEC and Contractor on remedial actions required; 5. Assess the effectiveness of Contractor's remedial actions; 6. If exceedance continues, arrange meeting with IEC and Supervisor /ER; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the Supervisor /ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues. 	<ol style="list-style-type: none"> 1. Discuss with ET and IEC on proper remedial actions; 2. Submit proposals for remedial actions to Supervisor /ER and IEC within three working day of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Limit Level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source and investigate the causes of exceedance; 2. Inform Contractor, IEC, Supervisor /ER, and EPD; 3. Repeat measurement to confirm finding; 4. Assess effectiveness of 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss possible remedial measures with ET and Contractor; 4. Advise the Supervisor /ER 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on proper remedial actions; 3. Submit proposal for remedial actions to Supervisor /ER and IEC

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results.	on the effectiveness of the proposed remedial measures.	4. Implemented; Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues.	within three working days of notification; 4. Implement the agreed proposals.
Limit Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Notify IEC, Supervisor /ER, Contractor and EPD; 2. Repeat measurement to confirm findings; 3. Carry out analysis of Contractor's working procedures to identify source and investigate the causes of exceedance; 4. Increase monitoring frequency to daily; 5. Arrange meeting with IEC, Supervisor /ER and Contractor to discuss the remedial action to be taken; 6. Assess effectiveness of Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results; 7. If exceedance stop, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with Supervisor /ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on proper remedial actions; 3. Submit proposal for remedial actions to Supervisor /ER and IEC within three working days of notification; 4. Implement the agreed proposals; 5. Submit further remedial actions if problem still not under control; 6. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated.

Appendix J – Calibration certificates, catalogue of noise monitoring equipment

Catalogue of Sound Level Meter

Specifications



	NL-52	NL-42
Applicable standards	IEC 61672-1: 2002 Class 1 ANSI S1.4-1983 Type 1 ANSI S1.4A-1985 Type 1 ANSI S1.43-1997 Type 1 JIS C 1509-1: 2005 Class 1	IEC 61672-1: 2002 Class 2 ANSI S1.4-1983 Type 2 ANSI S1.4A-1985 Type 2 ANSI S1.43-1997 Type 2 JIS C 1509-1: 2005 Class 2
Measurement functions	WEEE Directives, Chinese RoHS (export model for China only) Simultaneous measurement of the following items, with selected time weighting and frequency weighting	
Processing (main ch)	Instantaneous sound pressure level: L_p Equivalent continuous sound pressure level: L_{eq} Sound exposure level: L_E Maximum sound pressure level: L_{max} Minimum sound pressure level: L_{min} Percentile sound levels: L_N (0.1 to 99.9%, 0.1-increment steps, max. 5 values)	
Processing (sub ch)	Instantaneous sound pressure level: L_p	
Additional processing	In addition to main processing items, one of the following can be selected for simultaneous processing: C-weighted equivalent continuous sound level: L_{Ceq} C-weighted peak sound level: L_{Cpeak} Z-weighted peak sound level: L_{Zpeak} 1-time-weighted equivalent continuous sound level: $L_{A,eq}^{*2}$ Maximum 1-time-weighted equivalent continuous sound level: $L_{A,max}^{*2}$ The power average of the maximum level of each 5 second interval: L_{Aim}^{*2} of the sub-channel, so when the sub-channel has A weighting, L_{Aim} can be selected. When C-weighting (Z-weighting) is selected, the additional processing L_{Ceq} and L_{Cpeak} (L_{Zpeak}) are selectable.	
Measuring time	10 s, 1, 5, 10, 15, 30 m, 1, 8, 24 h, and manual (maximum 24 h)	
Microphone	Type UC-59 Sensitivity level -27 dB	Type UC-52 Sensitivity level -33 dB
Measurement range	A-weighting: 25 dB to 138 dB C-weighting: 33 dB to 138 dB Z-weighting: 38 dB to 138 dB C-weighting peak sound level: 55 dB to 141 dB Z-weighting peak sound level: 60 dB to 141 dB	
Inherent noise	A-weighting 17 dB or less C-weighting 25 dB or less Z-weighting 30 dB or less	19 dB or less 27 dB or less 32 dB or less
Frequency range	20 Hz to 20 kHz	
Frequency weighting	A, C, and Z	
Time weighting	F (Fast) and S (Slow)	
Level range	Single range (Linearity range: 113 dB)	
Bar graph display range max	Max. 110 dB (20 to 130 dB)	
Switching of bar graph display	Set the upper/lower limit in 10 dB increments.	
RMS detection circuit	Digital processing method	
Sampling cycle	20.8 μ s (L_p , L_{eq} , L_E , L_{max} , L_{min} , L_{peak} : sampling frequency: 48 kHz) 100 ms (L_N)	
Calibration	Measurement Law: electrical calibration performed according to IEC and JIS standards, using internally generated signals; acoustic calibration performed with the NC-74.	
Correction functions	Windscreen correction: Compliant with IEC 61672-1 and JIS C 1509-1 standards when the windscreen is installed. Diffuse sound field correction: Correction of frequency characteristics in order to comply with standards (ANSI S1.4) in diffuse sound field.	
Delay time	The meter can be set to start measuring a specified time (OFF, 1, 3, 5 or 10 s) after the start button has been pressed or when a user-set trigger is exceeded.	
Back erase function	When the PAUSE key is pressed or when a measurement, the preceding (user selectable) 0, 1, 3 or 5 s data are excluded from processing.	
Display	Backlit semi-transparent color TFT LCD display WQVGA (400 x 240 dots) * LCD with touch panel (Capacitive Touch Panel) Numerical display update frequency: 1 s Bar graph update frequency: 100 ms	
Store	Manual Data for measurement results are stored manually in single address increments. Internal memory: max. 1000 sets SD Card: depends on the capacity of the SD Card*1	
	Auto*2 Instantaneous values (L_p mode) and processed values (L_{eq} mode) are stored continuously and automatically at preset intervals. L_p sampling cycle 100 ms, 200 ms, 1 s, L_{eq} 1s L_{eq} sampling cycle 10 s, 1, 5, 10, 15, 30 ms, 1, 8, 24 h Measurement Time Max. 1000 h (depends on the capacity of the SD Card)*1	

Data recall	Allows viewing of stored data
Setup memory	Up to five setup configurations can be saved in internal memory, for later recall Start up via file settings previously stored on SD card possible
Waveform recording*3	
File format	Uncompressed waveform WAVE file
Sampling frequency	Select 48 kHz, 24 kHz or 12 kHz
Data length	Select 24 bit or 16 bit
Outputs	
DC output	Output DC signals using a frequency weighting characteristic selected by processing
Output voltage	2.5 V, 25 mV / dB at bar graph display full scale
AC output	Output AC signals using a frequency weighting characteristic selected by processing or by A, C, Z-weighting.
Output voltage	1 V (rms values) at bar graph display full scale
Comparator output*2	Turns on when the open-collector output exceeds the set value (max. applied voltage 24 V, max. current 60 mA, allowable dissipation 300 mW)
USB	Allows USB to be connected to a computer and recognized as a removable disk Allows USB to be controlled via communication commands
RS-232C communication	Allows for RS-232C communication via use of a dedicated cable
Data continuous output*2	
Type of data	L_p L_{eq} , L_{max} , L_{min} , L_{peak}
Output interval	100 ms
Print out	Printing of measurement results on dedicated printer DPU-414
Power requirements	Four IEC R6 (size AA) batteries (alkaline or rechargeable batteries) or external power supply
Battery life (23 °C)	Alkaline battery LR6 (AA) 26 h Ni-MH secondary battery: 25 h At the maximum * Depends on the setting
AC adapter	NC-98C (NC-34 for previous models cannot be used)
External power voltage	5 to 7 V (rated voltage: 6 V)
Current consumption	Approximately 90 mA (normal operation, rated voltage)
Ambient conditions	Temperature: -10 to +50 °C Humidity: 10 to 90 % RH (non-condensing)
Dustproof / water resistant performance*4	IP code: IP54 (except for microphone) See precautions regarding waterproofing
Dimensions, weight	Approx. 250 (H) x 76 (W) x 33 mm(D), approx. 400 g (with batteries)
Supplied accessories	Storage case x 1, Windscreen WS-10 x 1, Windscreen fall prevention rubber x 1, Hand strap x 1, LR6 (AA) alkaline batteries x 4, SD card 512 MB x 1 (NX-42EX pre-installed model only)

Options

	Product name	Product number
Extended function program (Inst. on 512 MB SD card)		NX-42EX
Waveform recording program*2 (Inst. on 2 GB SD card)		NX-42WR
Octave, 1/3 octave real-time analysis program*2 (Inst. on 512 MB SD card)		NX-42RT
FFT analysis program*2 (Inst. on 512 MB SD card)		NX-42FT
Data management software for environmental measurement		AS-60
Data management software for environmental measurement (Includes the octave and 1/3 octave data management software)		AS-60RT
Data management software for environmental measurement (Includes the vibration level data management software)		AS-60VM
Waveform analysis software		CAT-WAVE
SD Card 512 MB		SD-512M
SD Card 2 GB		SD-2G
AC adapter (100 V to 240 V)		NC-98C
Battery pack		BP-21
Microphone extension cables		EC-04 (from 2 m)
BNC-Pin output code		CC-24
Comparator output cable		CC-42C
Printer		DPU-414
Printer cable		CC-42P
RS-232C serial I/O cable		CC-42R
USB cable		—
Sound calibrator		NC-74
All-weather windscreen		WS-15
Windscreen mounting adapter		WS-15006
Rain protection windscreen		WS-16
Sound level meter tripod		ST-80
All-weather windscreen tripod		ST-81

*1 Use Rion fully guaranteed products. *2 NX-42EX required (sold separately). *3 NX-42WR required (sold separately). *4 Protection against harmful dust and water splashing from any direction.

Precautions regarding waterproofing

Before use, verify that the rubber bottom cover and the battery compartment lid are firmly closed.
To maintain the water and dust proof rating, internal packing replacement is required every two years (at cost).

* Windows is a trademark of Microsoft Corporation.
* Specifications subject to change without notice.

Distributed by:

This product is environment-friendly. It does not include toxic chemicals on our policy.
 This product is certified to an International Protection rating of IP54 (dust protected and resistant to splashing water).
This leaflet is printed with environmentally friendly vegetable-based ink on recycled paper.

1011-4 212 P.D




RION CO., LTD.
http://www.rion.co.jp/english/

3-20-41, Higashimotomachi, Kokubunji, Tokyo 185-8533, Japan
Tel: +81-42-359-7888 Fax: +81-42-359-7442

Calibration Certificate of Sound Level Meter

AAST-SLM-11
Cal Date: 29 July 2024



中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书

CALIBRATION CERTIFICATE

证书编号: 2HB24001410-0002
Certificate No. 




中国认可
国际互认
CALIBRATION
CNAS L13344

委托单位: Client	Castco Testing Centre Limited		
仪器名称: Description	Sound Level Meter		
型号规格: Model/Type	NL-52		
制造商: Manufacturer	Rion		
机身号: Serial No.	00976204		
管理号: Asset No.	AAST-SLM-11		
接收日期: Rec. Date	2024-07-18	校准日期: Cal. Date	2024-07-29
签发日期: App. Date	2024-07-30	建议校准周期: Reference Cal. Period	12个月(12 months)
结论: Conclusion	所校准项目符合技术要求(The calibrated items meet the technical requirements)		

校准: 赵文钊 赵文钊

签发: 郑木力 郑木力

检验: 钟灏 钟灏

印章: Stamp



扫一扫查真伪

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服热线: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhouchu Avenue West,Zengcheng District,Guangzhou,China
Add. of the Lab: No.78,Zhouchu Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 6 页
Page of

证书编号(Certificate No.): 2HB24001410-0002

说明

DIRECTIONS

- 本机构是国家市场监督管理总局授权建立的法定计量检定机构:“国家环境综合试验设备计量站”,国家国防科工局授权建立的“国防科技工业4412二级计量站”,本机构质量管理体系符合ISO/IEC 17025:2017标准的要求。
This laboratory is the legal metrological institute authorized by the State Administration for Market Regulation. It is the "Nation Metrology Station of Combined Environmental Testing Equipment". It is the "No. 4412 Class 2 Metrology Station of Science, Technology and Industry for National Defense" authorized by the State Administration of Science, Technology and Industry for National Defense. The quality management system of this laboratory is in accordance with the ISO/IEC 17025:2017.
- 本证书中的数据可溯源到国际单位制(SI)单位和/或社会公用计量标准。
The data of the certificate is traceable to the International system of Units (SI) and/or the public metrological standards.
- 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
* JJG 188-2017 声级计检定规程: Sound pressure level: (20~130)dB; Frequency Weighting: (20~130)dB, (10 Hz~20kHz)
* 详细内容请查看CNAS网站中注册编号为L13344的证书附件,超出范围的内容未被认可,其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)
- 本次校准所使用的主要测量标准及溯源性声明(The main measurement standards used during the calibration and traceability declaration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
前置放大器(2239842)	LSxx2024-02588/2025-03-12/中国计量院	频率响应: ±0.1dB	10Hz~50kHz
声校准器(2218291)	4GC23001017-0005/2025-01-29/赛宝(广州)	1级	94dB, 124dB@ (1000 Hz)
数字多用表(3146A63487)	4GC23000695-0001/2024-10-25/赛宝(广州)	直流电压: ±0.01%; 直流电 流: ±0.01%; 交流电压: ± 0.1%; 电阻: ±0.01%; 频 率: ±0.01%	10mV~100V (10Hz~200 kHz)
功率放大器(2536312)	4GC23000907-0001/2024-12-14/赛宝(广州)	失真度: ≤0.2%; 频率响应 : ±0.2dB	20Hz~50kHz
PULSE分析系统(3160-1 00186)	GFJGJL1001231007106/2024-10-24/航空 304所	频率: $U_{me} \pm 0.001\%$, $k=2$; 电压: $U_{me} \pm 0.10\%$, $k=2$	频率: 0.001Hz~51.2kHz, 电压: (1×10^{-3} ~30)V
正弦信号发生器(243165)	SXE202301878/2024-11-21/广东计量院	频率响应MPE±0.1dB	10Hz~50kHz
信号发生器(389052)	4GC24000402-0001/2025-05-13/赛宝(广州)	1.衰减器: 10dB改变量± 0.05dB; 1dB改变量±0.02dB; 2. 频率响应: 10Hz~ ; 0.1dB改变量±0.01dB; 2. 100kHz; 3.频率: 10Hz~ 频率响应±0.1dB; 3.失真度 ≤0.1%; 4.频率±0.25%; 5. 时间 (0.25~2000) ms 猝发声, 持续时间±1%	1.衰减器: (0~80) dB ; 2.频率响应: 10Hz~ ; 3.频率: 10Hz~ ; 4.猝发声: 持续 时间 (0.25~2000) ms
耦合腔(3081703)	SXE202483019/2026-02-04/广东计量院	失真度: <2%; 耦合端一致 性: ±0.3dB; 短期漂移: < 0.5dB; 工作有效声压级: ≥ 80dB	10Hz~20kHz
实验室标准声源(2246 093)	GFJGJL1001240306537/2025-03-17/航空 304所	LS级	10Hz~25kHz

计量溯源性声明(Metrological Traceability Declaration):

被校器具 Instrument	设备名称 Standard Name	外部机构/溯源证书编号 Institute/Certificate No.
Sound Level Meter	前置放大器	中国计量院/LSxx2024-02588
	声校准器	航空304所/GFJGJL1001230304185
	数字多用表	广东计量院/DBN202260767
	功率放大器	航空304所/GFJGJL1001231007106
	PULSE分析系统	航空304所/GFJGJL1001231007106
	正弦信号发生器	广东计量院/SXE202301878
信号发生器	航天514所/GFJGJL1004240400235	
耦合腔	广东计量院/SXE202483019	

第 2 页,共 6 页
Page of

Calibration Certificate of Sound Level Meter

Sound Level Meter	实验室标准传声器	航空304所/GFJGJL1001240306537
-------------------	----------	----------------------------

5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室

6. 环境条件(Environmental conditions):
温度(Temperature): 23.3°C 相对湿度(Relative Humidity): 66% 其它(Other): /

7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度评定与表示》评定,由合成标准不确定度乘以包含概率约为95%时对应的包含因子 k 得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.

8. 证书中“P”、“合格”代表“测量结果在允许范围内”,“F”、“不合格”代表“测量结果不在允许范围内”,“N/A”代表“不适用或技术指标暂时无法确认等”。本证书报告的结论仅供参考,使用人员应结合实际测量的要求合理使用,如考虑测量结果测量不确定度的影响等。
“P” and “Pass” in this certificate stand for “Low Limit<the measured value<High Limit”, “F” and “Fail” stand for “the measured value>Low Limit or the measured value>High Limit”, “N/A” stands for “Not Applicable or The technical specification has not been confirmed etc”. The conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.


9. 建议校准周期是本实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议,供委托方参考。委托方可以根据实际使用情况自行决定样品的校准周期。
The reference calibration period is based on the reference documents and normal operating conditions of the calibrated instrument. It is only for reference. The client may decide the calibration period of the instrument according to the actual use.

注:1.本证书未经本机构书面授权,不得部分复制。(The certificate shall not be partly reproduced without written approval of the laboratory.)
2.本次校准结果仅与被校物有关。(The results are only related to the items calibrated.)
3.“委托方”、“委托方联络信息”由委托方提供,“制造商”、“型号规格”、“出厂编号”以及“设备编号”为仪器上标注,委托方对上面内容如有异议,须在收到证书后二十个工作日内提出。
The information Client and Contact Information are provided by client, and the Manufacturer, Model/Type, Serial No. and Equipment No. are marked on the items. Client shall submit any objection within 20 working days after receiving the certificate for the information above.



CEPREI

第 3 页,共 6 页
Page of


证书编号(Certificate No.): 2HB24001410-0002

1 外观与工作正常性检查 (Appearance and Function Check)
无影响证书中测量结果准确度的因素和缺陷。
There are no factor and defect that affect the measurement result accuracy of the certificate.

2 指示声级调整 (Indication SPL Calibration) 频率(Frequency):1000Hz

传声器型号 (Microphone Type)	传声器编号 (Microphone SN.)	放大器型号 (Preamplifier Type)	放大器编号 (Preamplifier SN.)
/	/	/	/

声校准器型号 (Calibrator Type)	标准声压级 (Reference SPL) (dB)	调整前示值 (Before Adjust) (dB)	调整后示值 (After Adjust) (dB)
4231	94.0	94.4	94.0

3 级线性 (Level Linearity)

3.1 参考级量程 (Reference Range) 频率(Frequency): 8000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U ($k=2$) (dB)
130.0	129.9	-0.1	±0.8	P	0.3
129.0	128.9	-0.1	±0.8	P	0.3
128.0	127.9	-0.1	±0.8	P	0.3
127.0	126.9	-0.1	±0.8	P	0.3
126.0	125.9	-0.1	±0.8	P	0.3
125.0	124.9	-0.1	±0.8	P	0.3
120.0	119.9	-0.1	±0.8	P	0.3
110.0	110.0	0.0	±0.8	P	0.3
100.0	100.0	0.0	±0.8	P	0.3
90.0	90.0	0.0	±0.8	P	0.3
80.0	79.9	-0.1	±0.8	P	0.3
70.0	69.9	-0.1	±0.8	P	0.3
60.0	60.0	0.0	±0.8	P	0.3
50.0	49.9	-0.1	±0.8	P	0.3
40.0	39.9	-0.1	±0.8	P	0.3
35.0	34.8	-0.2	±0.8	P	0.3
34.0	33.8	-0.2	±0.8	P	0.3
33.0	32.9	-0.1	±0.8	P	0.3
32.0	31.8	-0.2	±0.8	P	0.3
31.0	30.8	-0.2	±0.8	P	0.3
30.0	29.8	-0.2	±0.8	P	0.3

第 4 页,共 6 页
Page of
数据页(Data sheet) ID: 071288

Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB24001410-0002

3.2 其它级量程 (Other Range)

频率(Frequency): 1000Hz

标准声级 (Standard) (dB)	指示声级 (Indication) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U ($k=2$) (dB)
130.0	129.9	-0.1	± 0.8	P	0.3
129.0	128.9	-0.1	± 0.8	P	0.3
128.0	127.9	-0.1	± 0.8	P	0.3
127.0	126.9	-0.1	± 0.8	P	0.3
126.0	125.9	-0.1	± 0.8	P	0.3
125.0	124.9	-0.1	± 0.8	P	0.3
120.0	119.9	-0.1	± 0.8	P	0.3
110.0	110.0	0.0	± 0.8	P	0.3
100.0	100.0	0.0	± 0.8	P	0.3
90.0	90.0	0.0	± 0.8	P	0.3
80.0	80.0	0.0	± 0.8	P	0.3
70.0	70.0	0.0	± 0.8	P	0.3
60.0	60.0	0.0	± 0.8	P	0.3
50.0	50.0	0.0	± 0.8	P	0.3
40.0	40.0	0.0	± 0.8	P	0.3
35.0	34.9	-0.1	± 0.8	P	0.3
34.0	33.9	-0.1	± 0.8	P	0.3
33.0	32.8	-0.2	± 0.8	P	0.3
32.0	31.8	-0.2	± 0.8	P	0.3
31.0	30.8	-0.2	± 0.8	P	0.3
30.0	29.8	-0.2	± 0.8	P	0.3



Calibration Certificate of Sound Calibrator

证书编号(Certificate No.): 21(B2400)796-0001

说明 DIRECTIONS

1. 本机构是国家市场监督管理总局授权建立的法定计量检定机构：“国家环境综合试验设备计量站”，国家国防科工局授权建立的“国防科技工业4412二级计量站”，本机构质量管理体系符合ISO/IEC 17025:2017标准的要求。
This laboratory is the legal metrological institute authorized by the State Administration for Market Regulation. It is the "Nation Metrology Station of Combined Environmental Testing Equipment". It is the "No. 4412 Class 2 Metrology Station of Science, Technology and Industry for National Defense" authorized by the State Administration of Science, Technology and Industry for National Defense. The quality management system of this laboratory is in accordance with the ISO/IEC: 17025:2017.
2. 本证书中的数据可溯源到国际单位制(SI)单位和/或社会公用计量标准。
The data of the certificate is traceable to the International system of Units (SI) and/or the public metrological standards.
3. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
▪ JJG 176-2022 声校准器检定规程: Sound Pressure Level: 94dB, 104dB, 114dB, 124dB, (63Hz~16kHz); Frequency: 31.5Hz~16kHz; Distortion: 0.01%~30%
* 详细内容请查看CNAS网站中注册编号为L13344的证书附件。超出范围的内容未被认可。其结果结论所依赖的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)
4. 本次校准所使用的主要测量标准及溯源性声明(The main measurement standards used during the calibration and traceability declaration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
前置放大器(2239843)	L.Sx2024-04011/2025-04-20/中国计量院	频率响应±0.1dB	(10~50000) Hz
Pulse分析仪(3160-10018)	4GC24000729-0003/2025-07-29/赛宝(广州)6)	频率: $f_{min}=0.001\%$, $f_{max}=2$;电压: $U_{min}=0.10\%$, $k=2$	频率:0.001Hz~51.2kHz;电压: $(1 \times 10^{-3} \sim 30)V$
数字多用表(MY4505167)	GFJGJL1004240400234/2025-03-11/航天514所	直流电压: $\pm 1 \times 10^{-4}$; 直流电流: $\pm 1 \times 10^{-4}$; 交流电压: $\pm 0.1\%$; 交流电流: $\pm 0.1\%$; 电阻: $\pm 1 \times 10^{-4}$	直流电压: $\pm 10mV \sim \pm 1000V$; 直流电流: $\pm 10\mu A \sim \pm 1A$; 交流电压: $(10mV \sim 700V)$ @ (1 Hz~1MHz); 交流电流: (3mA~1A) @ (10Hz~10kHz); 电阻: $10\Omega \sim 10M\Omega$
实验室标准传声器(2246)	L.Sx2024-04498/2025-04-18/中国计量院(093)	LS级	10Hz~25kHz

计量溯源性声明(Metrological Tracability Declaration):

被校准器具 Instrument	设备名称 Standard Name	外部机构/溯源证书编号 Institute/Certificate No.
Sound Level Calibrator	前置放大器	中国计量院/L.Sx2024-04011
	Pulse分析仪	广东计量院/SXE202301878
	数字多用表	航天514所/GFJGJL1004240400234
	实验室标准传声器	中国计量院/L.Sx2024-04498

5. 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室
6. 环境条件(Environmental conditions):
温度(Temperature): 23.7°C 相对湿度(Relative Humidity): 63% 其它(Other): /
7. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度评定与表示》评定，由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.


Calibration Certificate of Sound Calibrator



AAGT-SLC-05
Cal Date: 30 July 2024

中国赛宝实验室计量检测中心
(工业和信息化部电子第五研究所计量检测中心)
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

校准证书

CALIBRATION CERTIFICATE

证书编号: 2HB24001410-0003
Certificate No. 

  中国认可
国际互认
校准
CALIBRATION
CNAS L13344

委托单位: Casteo Testing Centre Limited
Client

仪器名称: Sound Level Calibrator
Description

型号规格: NC-74
Model/Type

制造商: Rion
Manufacturer

机身号: 34178129
Serial No.



管理号: AAST-SLC-05
Asset No.

接收日期: 2024-07-18 校准日期: 2024-07-30
Rec. Date Cal. Date

签发日期: 2024-07-31 建议校准周期: 12个月(12 months)
App. Date Reference Cal. Period

结论: 所校准项目符合技术要求(The calibrated items meet the technical requirements)
Conclusion

校准: 赵文钰 赵文钰 检验: 钟灏 钟灏
Calibrated by Inspected by

签发: 郑木力 郑木力 印章:  印章: 
Approved by Stamp Stamp

扫一扫查真伪

赛宝计量检测中心
总部地址: 广州市增城区朱村街朱村大道西78号
实验室地址: 广州市增城区朱村街朱村大道西78号
客服电话: 020-87237633 传真: 020-87236189
投诉电话: 020-87236896
邮件: cal@ceprei.com
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre
HQ Addr: No.78,Zhuancun Avenue West,Zengcheng District,Guangzhou,China
Add of the Lab: No.78,Zhuancun Avenue West,Zengcheng District,Guangzhou,China
Service Tel: 020-87237633 Fax: 020-87236189
Complaint Tel: 020-87236896
Email: cal@ceprei.com
Website: www.ceprei-cal.com

第 1 页,共 4 页
Page of

证书编号(Certificate No.): 2HB24001410-0003

说明

DIRECTIONS

- 本机构是国家市场监督管理总局授权建立的法定计量检定机构;“国家环境综合试验设备计量站”,国家国防科工局授权建立的“国防科技工业4412二级计量站”,本机构质量管理体系符合ISO/IEC 17025:2017标准的要求。
This laboratory is the legal metrological institute authorized by the State Administration for Market Regulation. It is the “Nation Metrology Station of Combined Environmental Testing Equipment”. It is the “No. 4412 Class 2 Metrology Station of Science, Technology and Industry for National Defense” authorized by the State Administration of Science, Technology and Industry for National Defense. The quality management system of this laboratory is in accordance with the ISO/IEC 17025:2017.
- 本证书中的数据可溯源到国际单位制(SI)单位和/或社会公用计量标准。
The data of the certificate is traceable to the International system of Units (SI) and/or the public metrological standards.
- 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):
* JJG 176-2022 声校准器检定规程; Sound Pressure Level: 94dB、104dB、114dB、124dB(63Hz~8kHz); 94dB、104dB、114dB,(31.5Hz~16kHz); Frequency: 31.5Hz~16kHz; Harmonic Distortion: 0.1%~10%; (20Hz~20kHz)
* 详细内容请查看CNAS网站中注册编号为L13344的证书附件,超出范围的内容未被认可,其结果/结论所依据的合格评定活动不在认可范围内。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited, the conformity assessment activities on which the results/conclusions are based are outside the scope of accreditation.)
- 本次校准所使用的主要测量标准及溯源性声明(The main measurement standards used during the calibration and traceability declaration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
实验室标准传声器(2246 093)	GFJGJL1001240306537/2025-03-17/航空304所	LS级	10Hz~25kHz
前置放大器(2239842)	LSsx2024-02588/2025-03-12/中国计量院	频率响应: ±0.1dB	10Hz~50kHz
PULSE分析系统(3160-1 00186)	GFJGJL1001231007106/2024-10-24/航空304所	频率: $U_{100}=0.001\%$, $k=2$; 电压: $U_{100}=0.10\%$, $k=2$	频率: 0.001Hz~51.2kHz, 电压: $(1 \times 10^{-3} \sim 30)V$
数字多用表(3146A63487)	4GC23006695-0001/2024-10-25/赛宝(广州)	直流电压: ±0.01%; 直流电流: ±0.01%; 交流电压: ±0.1%; 电阻: ±0.01%; 频率: ±0.01%	10mV~100V (10Hz~200 kHz)

计量溯源性声明(Metrological Traceability Declaration):

被校准器具 Instrument	设备名称 Standard Name	外部机构/溯源证书编号 Institute/Certificate No.
Sound Level Calibrator	实验室标准传声器	航空304所/GFJGJL1001240306537
	前置放大器	中国计量院/LSsx2024-02588
	PULSE分析系统	航空304所/GFJGJL1001231007106
	数字多用表	广东计量院/DBN202260767

- 校准地点(The calibration place):
广州市增城区朱村街朱村大道西78号9栋110室
- 环境条件(Environmental conditions):
温度(Temperature): 24.2°C 相对湿度(Relative Humidity): 62% 其它(Other): /
- 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度评定与表示》评定,由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 “Evaluation and Expression of Uncertainty in Measurement”, and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.

第 2 页,共 4 页
Page of

Calibration Certificate of Sound Calibrator



证书编号(Certificate No.): 2HB24001410-0003

1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中测量结果准确度的因素和缺陷。

There are no factor and defect that affect the measurement result accuracy of the certificate.

2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	接受限 (Limit)	结论 (Pass/Fail)	U (k=2)
(dB)	(dB)	(dB)	(dB)		(dB)
94	94.06	0.06	≤0.25	P	0.10

3 频率 (Frequency)

规定频率 (Prescribed Fre.)	测量频率 (Measured Fre.)	频率误差的绝对值 (Absolute value of Fre.)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (k=2)
(Hz)	(Hz)	(%)	(%)		(%)
1000	1002.1	0.21	≤0.70	P	0.10

4 总失真+噪声 (Distortion and noise)

规定声压级 (Prescribed SPL)	规定频率 (Measured Fre.)	总失真+噪声 (Distortion and noise)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (k=2)
(dB)	(Hz)	(%)	(%)		(%)
94	1000	0.68	≤2.50	P	5.0

以下空白/No data hereafter



证书编号(Certificate No.): 2HB23001715-0001

1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中测量结果准确度的因素和缺陷。

There are no factor and defect that affect the measurement result accuracy of the certificate.

2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	接受限 (Limit)	结论 (Pass/Fail)	U (k=2)
(dB)	(dB)	(dB)	(dB)		(dB)
94	93.86	0.14	≤0.25	P	0.10

3 频率 (Frequency)

规定频率 (Prescribed Fre.)	测量频率 (Measured Fre.)	频率误差的绝对值 (Absolute value of Fre.)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (k=2)
(Hz)	(Hz)	(%)	(%)		(%)
1000	1003.7	0.37	≤0.70	P	0.10

4 总失真+噪声 (Distortion and noise)

规定声压级 (Prescribed SPL)	规定频率 (Measured Fre.)	总失真+噪声 (Distortion and noise)	接受限 (Limit)	结论 (Pass/Fail)	U_{rel} (k=2)
(dB)	(Hz)	(%)	(%)		(%)
94	1000	0.69	≤2.50	P	5.0

以下空白/No data hereafter

Catalogue of Air Flow Meter (TSI TA440)

SPECIFICATIONS

THERMAL ANEMOMETERS MODELS TA410, TA430 AND TA440

Velocity

Range (TA410)	0 to 20 m/s (0 to 4,000 ft/min)
Range (TA430, TA440)	0 to 30 m/s (0 to 6,000 ft/min)
Accuracy (TA410) ^{1,2}	±5% of reading or ±0.025 m/s (±5 ft/min), whichever is greater
Accuracy (TA430, TA440) ^{1,2}	±3% of reading or ±0.015 m/s (±3 ft/min), whichever is greater
Resolution	0.01 m/s (1 ft/min)

Duct Size (TA430, TA440)

Dimensions	1 to 635 cm in increments of 0.1 cm (1 to 250 inches in increments of 0.1 in.)
------------	--

Volumetric Flow Rate (TA430, TA440)

Range	Actual range is a function of velocity, and duct size
-------	---

Temperature

Range (TA410, TA430)	-18 to 99°C (0 to 200°F)
Range (TA440)	-10 to 60°C (14 to 140°F)
Accuracy ³	±0.3°C (±0.5°F)
Resolution	0.1°C (0.1°F)

Relative Humidity (TA440 only)

Range	5 to 95% RH
Accuracy ⁴	±3% RH
Resolution	0.1% RH

Wet Bulb Temperature (TA440 only)

Range	5 to 60°C (40 to 140°F)
Resolution	0.1°C (0.1°F)

Dew Point (TA440 only)

Range	-15 to 49°C (5 to 120°F)
Resolution	0.1°C (0.1°F)

Instrument Temperature Range

Operating (Electronics)	5 to 45°C (40 to 113°F)
Model TA410, TA430	-18 to 99°C (0 to 200°F)
Operating (Probe)	-10 to 60°C (14 to 140°F)
Model TA440	-10 to 60°C (14 to 140°F)
Storage	-20 to 60°C (-4 to 140°F)

Data Storage Capabilities (TA430, TA440)

Range	12,700+ samples and 100 test IDs
-------	----------------------------------

Logging Interval (TA430, TA440)

1 second to 1 hour

Specifications subject to change without notice.

TSI and the TSI logo are registered trademarks, and Airflow, the Airflow logo and LogDat2 are trademarks of TSI Incorporated.



Airflow Instruments, TSI Instruments Ltd.
Visit our website at www.airflowinstruments.co.uk for more information.

UK Tel: +44 149 4 459200 **Germany** Tel: +49 241 523030
France Tel: +33 491 11 87 64

P/N 2990548 Rev D (A4) ©2014 TSI Incorporated

Time Constant (TA430, TA440)

User selectable

External Meter Dimensions

8.4 cm x 17.8 cm x 4.4 cm (3.3 in. x 7.0 in. x 1.8 in.)

Meter Weight with Batteries

0.27 kg (0.6 lbs.)

Meter Probe Dimensions

Probe Length	101.6 cm (40 in.)
Probe Diameter of Tip	7.0 mm (0.28 in.)
Probe Diameter of Base	13.0 mm (0.51 in.)

Articulating Probe Dimensions

Articulating Section Length	19.7 cm (7.8 in.)
Diameter of Articulating Knuckle	9.5 mm (0.39 in.)

Power Requirements

Four AA-size batteries or AC adapter

	TA410	TA430, TA430-A	TA440, TA440-A
Velocity range 0 to 20.00 m/s (0 to 4000 ft/min)	+		
Velocity range 0 to 30.00 m/s (0 to 6000 ft/min)		+	+
Temperature	+	+	+
Flow		+	+
Humidity, wet bulb, dew point			+
Probe	Straight	Straight or -A articulated	Straight or -A articulated
Variable time constant		+	+
Manual data logging		+	+
Auto save data logging			+
Statistics		+	+
Review data		+	+
LogDat2 downloading software		+	+
Free Certificate of Calibration	+	+	+

¹Temperature compensated over an air temperature range of 5 to 65°C (40 to 150°F).

²The accuracy statement begins at 30 ft/min through 4000 ft/min (0.15 m/s through 20 m/s) for the Model TA410, and 50 ft/min through 6,000 ft/min (0.15 m/s through 30 m/s) for Models TA430 and TA440.

³Accuracy with instrument case at 25°C (77°F); add uncertainty of 0.03°C (0.05°F) for change in test ambient temperature.

⁴Accuracy with probe at 25°C (77°F). Add uncertainty of 0.2% RH/°C (0.1% RH/°F) for change in probe temperature; includes 1% hysteresis.

Calibration Certificate of Air Flow Meter



Cal Lab Limited 校正實驗室有限公司

Room 2103, Technology Plaza, 29-35 Sha Tsui Road,
Tuen Wan, NT, Hong Kong
Tel: +852 25680106 Email: info@callab.com.hk
Fax: +852 30116194 Website: www.callab.com.hk



Calibration Certificate No.: CC0022403

Information provided by customer

Customer: Castco Testing Centre Limited
Address: 33, On Kai Street, Fanling, N.T.

Equipment Identification provided by customer

Equipment Description	Manufacturer	Model No.	Serial No.	Assigned equipment No.
Air Velocity Monitor	TSI	AIRFLOW TA440	TA4401706003	TA4401706003

Certificate Information

Date of Receipt:	1 March 2024	Calibration Condition:	21.0°C, 54%RH, 1013hPa
Date of Calibration:	6 March 2024	Adjustment:	N/A
Due Date of Calibration:	N/A	Appearance:	Good
Calibration Procedure:	SOP-112	Remark:	N/A

Reference Equipment Identification

Equipment Description	Model	Serial No.	Expiration Date
Hot Wire Anemometer	9535	T95351316004	11 August 2024

Result of Calibration

Air Velocity	Reference Reading (m/s)	Measured Reading (m/s)	Error (m/s)	Uncertainty (%)	Technical Requirement	Technical Reference Doc.
	0.99	1.01	0.02	3.6	± 3 %	Mfr's Spec.
	2.01	2.00	-0.01	3.6	± 3 %	Mfr's Spec.
	5.02	5.05	0.03	3.6	± 3 %	Mfr's Spec.
	8.00	8.03	0.03	3.6	± 3 %	Mfr's Spec.

CT-RR-01

Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimate to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy at good condition.

Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.

Note4: The result shown in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.

Note5: Calibration item/parameter marked with * is out of scope of Cal Lab Limited (ASIA 3815.01).

Calibrated By:

Wing Cheng

Checked and Approved By:

Warren Yeung

Company Chop:



Certificate Issue Date: 6 March 2024

CT-RR-04

*** End of Certificate ***

- The certificate shall not be reproduced except in full, without written approval of Cal Lab Limited. CC0022403
- The certificate is issued subject to the latest Terms and Conditions, available at our web site. Page 1 of 1.

Appendix K – Noise monitoring results and graphical presentation


M4(A) – Le Billionnaire

Date	Temp (°C)	Wind Speed m/s	Weather	Measured Noise Level at M4(A), dB(A)						Limit	
				Time		Baseline	L _{Aeq}	L _{A10}	L _{A90}		
03/02/2025	17.8	0.4	Sunny	9:05	-	9:35	69.5	73.1	74.2	71.0	75
14/02/2025	16.3	0.6	Sunny	13:20	-	13:50	69.5	73.0	75.3	71.2	75
20/02/2025	18.6	0.3	Cloudy	11:30	-	12:00	69.5	72.9	74.0	70.9	75
26/02/2025	18.3	0.7	Sunny	13:00	-	13:30	69.5	73.3	74.6	71.0	75
								Maximum		73.3	
								Minimum		72.9	
								Average		73.1	


M5(A) – Prince Ritz

Date	Temp (°C)	Wind Speed m/s	Weather	Measured Noise Level at M5(A), dB(A)						Limit	
				Time		Baseline	L _{Aeq}	L _{A10}	L _{A90}		
03/02/2025	17.8	2.3	Sunny	11:20	-	11:50	72.5	74.6	76.8	72.0	75
14/02/2025	16.3	2.1	Sunny	15:35	-	16:05	72.5	74.1	76.0	72.4	75
20/02/2025	18.6	1.6	Cloudy	15:30	-	16:00	72.5	74.5	76.6	71.7	75
26/02/2025	18.3	1.3	Sunny	15:00	-	15:30	72.5	74.2	76.1	71.5	75
								Maximum		74.6	
								Minimum		74.1	
								Average		74.4	

L_{Aeq, 30-min} graphical results of M4(A) – Le Billionnaire

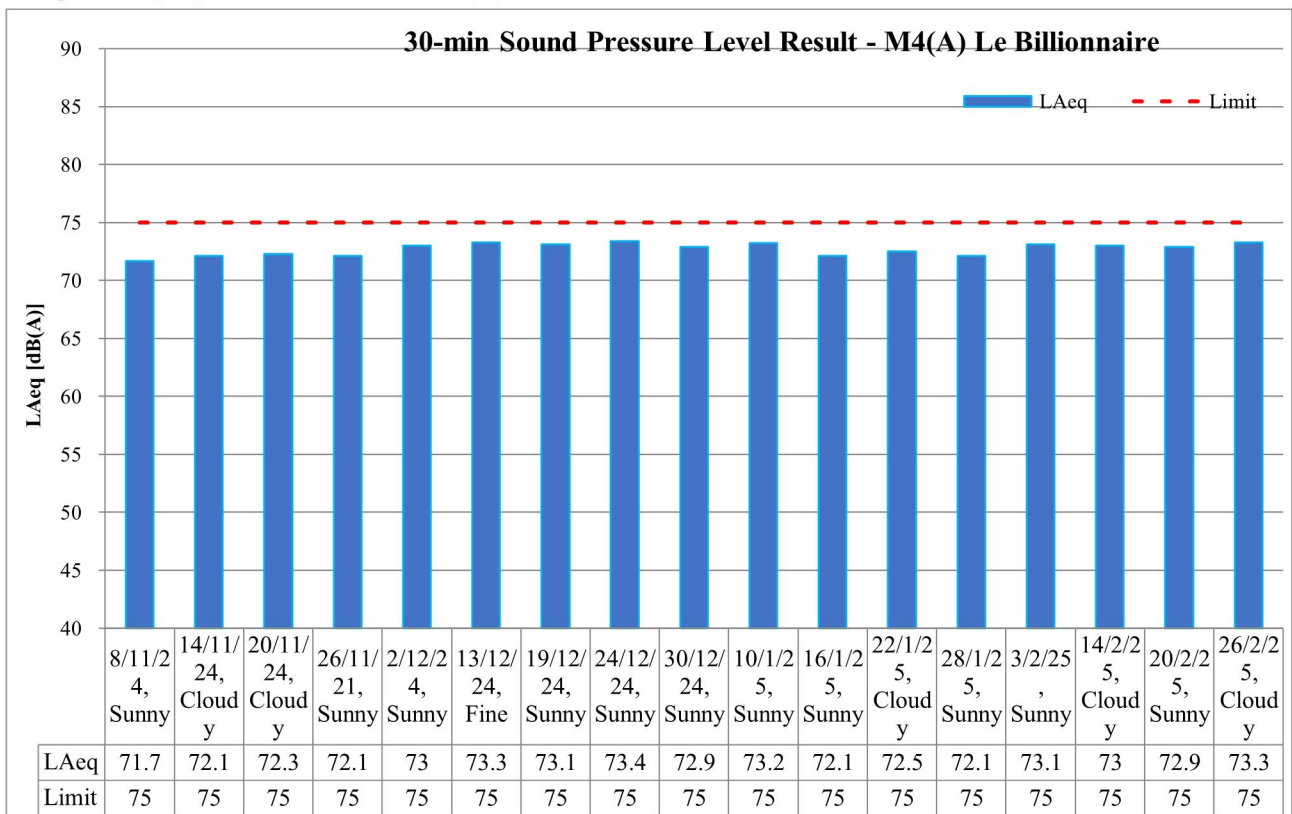

L_{Aeq, 30-min} graphical results of M5(A) – Prince Ritz

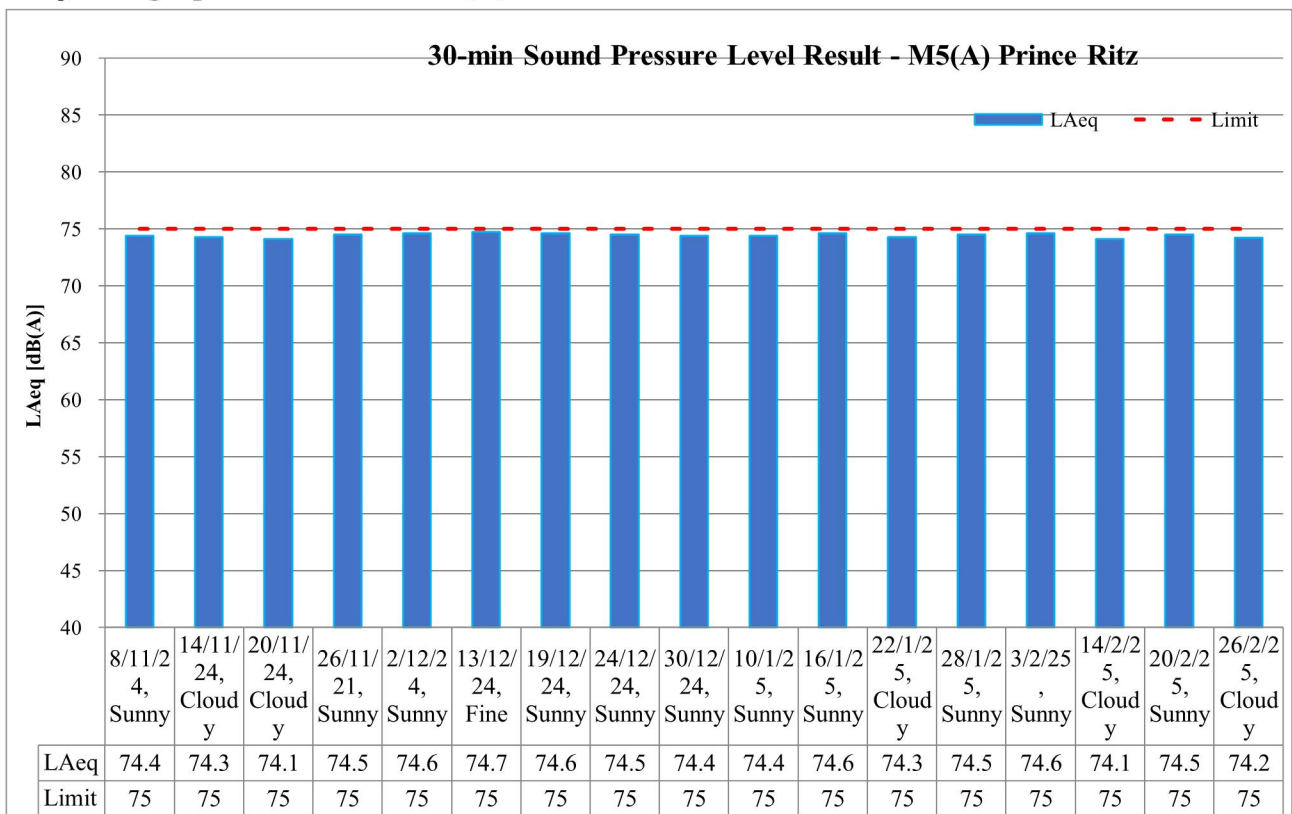

Major Construction Activities	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Floor screeding works at deck level of LW-02	✓	✓		
Backfilling at retaining wall for S14	✓	✓		
Construction works for DCS	✓	✓	✓	✓
Construction of LW02 structural steel roof	✓	✓		
Construction of Parapet for S14	✓	✓	✓	✓
Construction of bridge deck of S14	✓	✓	✓	
Construction of headwall at Subway SB01 Retrieval Shaft	✓	✓	✓	✓
Drainage construction and backfilling works for retaining wall of S14	✓			
Drainage construction works at PS2 and PS3	✓	✓	✓	✓
Renovation works for Subway KS10 Lift and Staircase	✓	✓	✓	✓
Renovation works for existing subways KS10	✓			
Road and Drain Construction works for Road L16, Commercial Street and Road D1	✓	✓	✓	✓
Tiling works at LW02	✓	✓	✓	✓
Tiling works at LW-02 and Subway KS10	✓	✓		
Lift installation at LW-02 and KS10	✓	✓		
Installation of glass panel and aluminum panels of LW02	✓	✓	✓	✓
Installation of glass balustrade at LW02	✓			
Installation of drainage system of pump house for KS10	✓	✓		
Ceiling painting and plastering inside Subway SB-01	✓	✓	✓	✓
Installation of VE panel sub-frame in Subway SB-01	✓			
Lift installation at LW02 and KS10	✓	✓	✓	✓
Demolition of existing parapet of K73	✓	✓	✓	✓
SB01 Sa Po Rd Retrieval Shaft Headwall RC construction	✓	✓	✓	✓
Installation of lighting system at LW-02		✓	✓	✓
Refurbishment for Bridge K73		✓	✓	✓
Drainage construction of S14		✓	✓	✓
Dismantling of portal frame at Bridge K73		✓		
Installation of steel formwork for curved top slab of headwall at Retrieval Shaft of Subway SB-01		✓	✓	
Watermain and road works at PS3		✓	✓	✓
Installation of cable tray at LW-02			✓	✓
Installation of glass balustrade at bridge deck of LW02			✓	✓
Installation of geotextile and subsoil drainage for planters at LW02			✓	✓
Installation of movement joint for S14			✓	✓
Installation of canopy at LW-02				✓
Asphalt application at S14			✓	✓

Factors might affect the monitoring results	Reporting Period			
	Nov 2024	Dec 2024	Jan 2025	Feb 2025
Non-project related construction activities in the adjacent construction sites were observed.	✓	✓	✓	✓

Appendix L – Event and Action Plan for noise

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded	<ol style="list-style-type: none"> 1. Notify Supervisor / ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, Supervisor / ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures submitted by the Contractor and advise the ER accordingly; 3. Advise the Supervisor / ER on the proposed remedial measures. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> 1. Submit noise mitigation proposal to IEC and Supervisor / ER; 2. Implement noise mitigation proposals. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>
Limit Level being exceeded	<ol style="list-style-type: none"> 1. Inform IEC, Supervisor /ER, Contractor and EPD; 2. Repeat measurement to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contract's working procedure; 6. Discuss remedial measures required with the IEC, Contractor and Supervisor /ER; 7. Assess effectiveness of 	<ol style="list-style-type: none"> 1. Discuss the potential remedial actions with Supervisor /ER, ET and Contractor; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and Supervisor /ER within 3 working days of notification; 3. Implement the agreed proposal; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated. <p>(The above actions should be</p>

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	<p>Contractor's remedial actions and keep IEC, EPD, and Supervisor /ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified.)</p>		<p>exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<p>taken within 2 working days after the exceedance is identified.)</p>

Appendix M – Event and Action Plan for Landscape and Visual Impact

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Design Check	<ol style="list-style-type: none"> 1. Check final design conforms to the requirements of EP and prepare report. 	<ol style="list-style-type: none"> 1. Check report. 2. Recommend remedial design if necessary. 	<ol style="list-style-type: none"> 1. Undertake remedial design if necessary. 	
Non-conformity on one occasion	<ol style="list-style-type: none"> 1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 4. Monitor remedial actions until rectification has been completed. 	<ol style="list-style-type: none"> 1. Check report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Check implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Notify Contractor. 2. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.
Repeated Non-conformity	<ol style="list-style-type: none"> 1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Increase monitoring frequency. 4. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 5. Monitor remedial actions until rectification has been completed. 6. If non-conformity stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Notify Contractor. 2. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.

Appendix N – Waste Flow Table

MONTHLY SUMMARY WASTE FLOW TABLE FOR 2025 (YEAR)

Month	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated A + B	Broken Concrete Generated A	General fill Generated B	Broken Concrete Reused in the Contract	General Fill Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Import Fill	Metals	Paper / Cardboard Packaging	Plastics (3)	Chemical Waste	Other, e.g. general refuse
	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000m ³]
JAN	3.55	0.00	3.55	0.00	0.50	0.00	3.05	0.00	0.00	0.00	0.00	0.00	0.20
FEB	2.00	0.00	2.00	0.00	0.70	0.00	1.30	0.00	0.00	0.00	0.00	0.00	0.35
MAR													
APR													
MAY													
JUNE													
SUB-TOTAL	5.55	0.00	5.55	0.00	1.20	0.00	4.35	0.00	0.00	0.00	0.00	0.00	0.55
JULY													
AUG													
SEPT													
OCT													
NOV													
DEC													
TOTAL	5.55	0.00	5.55	0.00	1.20	0.00	4.35	0.00	0.00	0.00	0.00	0.00	0.55

Appendix O – Environmental Mitigation Implementation Schedule (EMIS)

EIA Ref	Recommended Mitigation Measures	Implementation			
Part B Water Quality		Not Observed	Yes	No	Remark
S8.8	Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include use of sediment traps and adequate maintenance of drainage systems to prevent flooding and overflow	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms. Particular attention should be paid to the control of silty surface runoff during storm events.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and wash water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S8.8	<i>Drainage</i> On-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	<i>Sewage Effluent</i> Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	<i>Stormwater Discharges</i> Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	<i>Debris and Litter</i> In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

EIA Ref	Recommended Mitigation Measures	Implementation			
	is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur				
S8.8	Construction Works at or in Close Proximity of Storm Culvert or Seafront The proposed works should preferably be carried out within the dry season where the flow in the drainage channel /storm culvert/ nullah is low.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	The use of less or smaller construction plants may be specified to reduce the disturbance to the bottom sediment at the drainage channel /storm culvert / nullah.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S8.8	Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S8.8	Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Mitigation measures to control site runoff from entering the nearby water environment should be implemented to minimize water quality impacts. Surface channels should be provided along the edge of the waterfront within the work sites to intercept the runoff.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Construction effluent, site run-off and sewage should be properly collected and/or treated.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Any works site inside the storm water courses should be temporarily isolated, such as by placing of sandbags or silt curtains with lead edge at bottom and properly supported props to prevent adverse impact on the storm water quality.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Silt curtain may be installed around the construction activities at the seafront to minimize the potential impacts due to accidental spillage of construction materials.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert/drainage channel/sea.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S8.8	Supervisory staff should be assigned to station on site to closely supervise and monitor the works	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Part C Construction Noise Impact		Not Observed	Yes	No	Remark
S7.8	Use of quiet PME, movable barriers for Asphalt Paver, Breaker, Excavator and Hand-held breaker and full enclosure for Air Compressor, Bar Bender, Concrete Pump, Generator and Water Pump	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S7.9	Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program. Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program. Mobile plant, if any, should be sited as far away from NSRs as possible.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Part D Waste / Chemical Management		Not Observed	Yes	No	Remark
S5.2	Prepare a Waste Management Plan, which becomes a part of the Environmental Management Plan, in accordance with the requirements stipulated in ETWB TC(W) No. 19/2005, approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	Training of site personnel in site cleanliness, proper waste management and chemical waste handling procedures	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	Provision of sufficient waste disposal points and regular collection for waste. Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Separation of chemical wastes for special handling and appropriate treatment	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S9.5	1)Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site 2)Training of site personnel in proper waste management and chemical waste handling procedures 3)Provision of sufficient waste disposal points and regular collection for disposal 4)Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers 5)A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

EIA Ref	Recommended Mitigation Measures	Implementation			
S9.5	Waste Reduction Measures 1) Sort C&D waste from demolition of the remaining structures to recover recyclable portions such as metals 2) Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal 3) Encourage collection of aluminum cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force 4) Any unused chemicals or those with remaining functional capacity should be recycled 5) Proper storage and site practices to minimize the potential for damage or contamination of construction materials	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S9.5	Construction and Demolition Material Mitigation measures and good site practices should be incorporated into contract document to control potential environmental impact from handling and transportation of C&D material. The mitigation measures include: 1) Where it is unavoidable to have transient stockpiles of C&D material within the Project work site pending collection for disposal, the transient stockpiles should be located away from waterfront or storm drains as far as possible 2) Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric 3) Skip hoist for material transport should be totally enclosed by impervious sheeting 4) Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site 5) The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores 6) The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle 7) All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S9.5	When delivering inert C&D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S9.5	Chemical Waste After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Part E Landscape & Visual		Not Observed	Yes	No	Remark
S13.9	CM1 - All existing trees should be carefully protected during construction. CM2 - Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work. CM3 - Control of night-time lighting. CM4 - Erection of decorative screen hoarding.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Part F Air Quality		Not Observed	Yes	No	Remark
S6.8	Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S6.8	Misting for the dusty material should be carried out before being loaded into the vehicle.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S6.8	Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S6.8	The tarpaulin should be properly secured and should extend at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S6.8	The vehicles should be restricted to maximum speed of 10 km per hour and confined haulage and delivery vehicle to designated roadways insider the site. On-site unpaved roads should be compacted and kept free of lose materials	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S6.8	Vehicle washing facilities should be provided at every vehicle exit point	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S6.8	The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S6.8	Every main haul road should be sealed with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

EIA Ref	Recommended Mitigation Measures	Implementation			
S6.8	Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the three sides.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S6.8	Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S6.5	8 times daily watering of the work site with active dust emitting activities.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

**Appendix P – Summaries of Environmental Complaint, Warning,
Summon and Notification of Successful Prosecution**

Reporting Month: February 2025

Contract No.	Record of Complaint (Yes/No)	Record of Warning (Yes/No)	Notification of Summons and Successful Prosecutions (Yes/No)
ED/2018/05	No	No	No

Cumulative Statistics on Complaints, Notification of Summons and Successful Prosecutions upto reporting month

Contract No.	Record of Complaint	Record of Warning	Notification of Summons and Successful Prosecutions
ED/2018/05	1	0	0
