


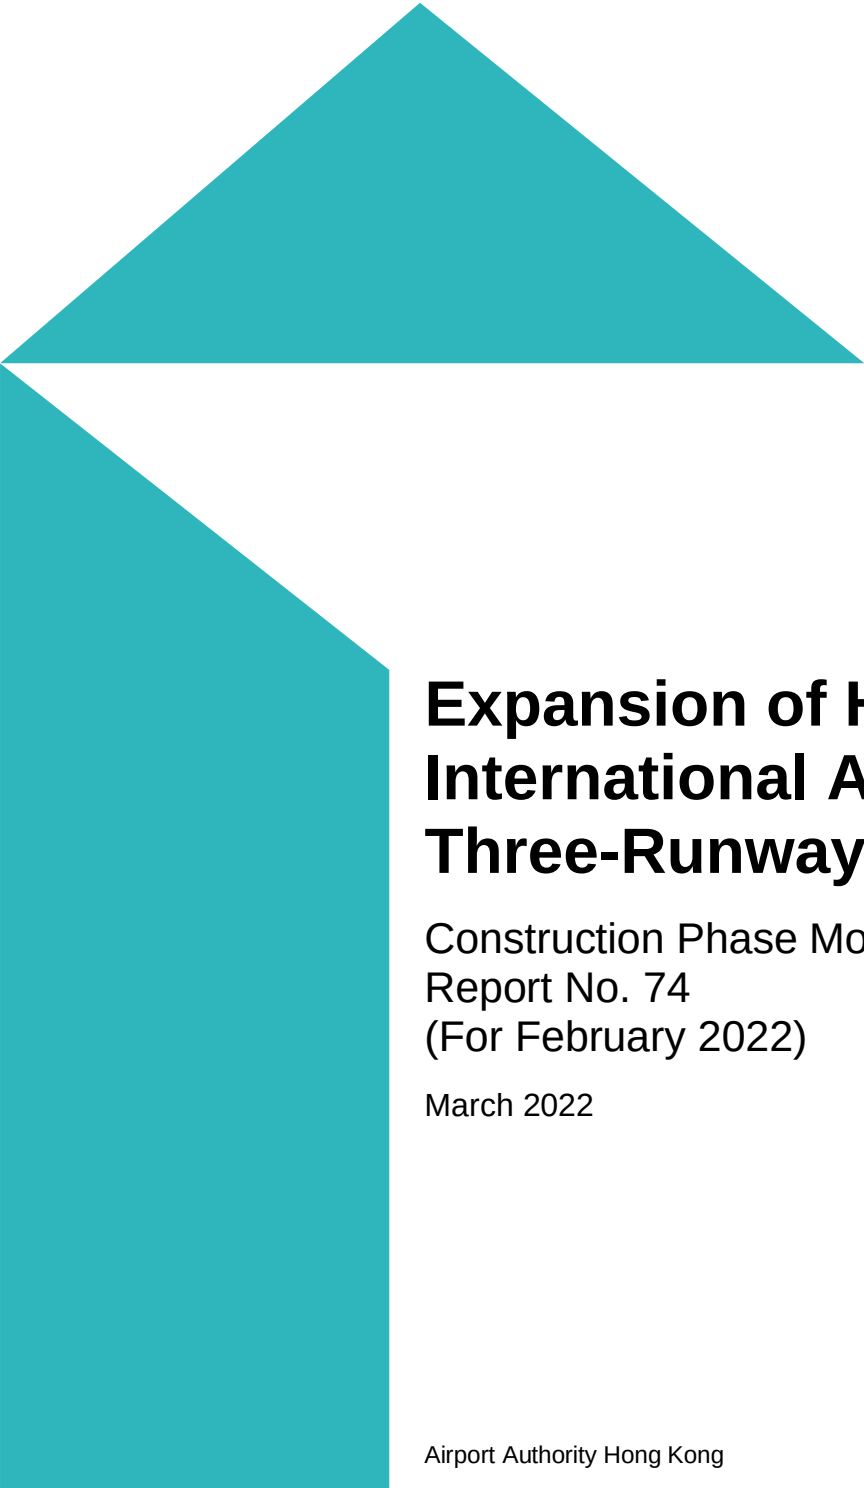

Expansion of Hong Kong International Airport into a Three-Runway System

Construction Phase Monthly EM&A
Report No. 74
(For February 2022)

March 2022

Mott MacDonald
3/F Manulife Place
348 Kwun Tong Road
Kwun Tong
Kowloon
Hong Kong

T +852 2828 5757
mottmac.hk

Expansion of Hong Kong International Airport into a Three-Runway System

Construction Phase Monthly EM&A
Report No. 74
(For February 2022)

March 2022

This Monthly EM&A Report No. 74 has been reviewed and certified by

the Environmental Team Leader (ETL) in accordance with

Condition 3.5 of Environmental Permit No. EP-489/2014.

Certified by:

A handwritten signature in black ink, appearing to read 'Terence Kong', is positioned above a horizontal line.

Terence Kong
Environmental Team Leader (ETL)
Mott MacDonald Hong Kong Limited

Date

14 March 2022



AECOM
12/F, Grand Central Plaza, Tower
2, 138 Shatin Rural Committee
Road, Shatin, Hong Kong
香港新界沙田鄉事會路 138 號新城
市中央廣場第 2 座 12 樓
www.aecom.com

+852 3922 9000 tel

+852 3922 9797 fax

Our Ref : 60440482/C/JCHL220314

By Email

Airport Authority Hong Kong
HKIA Tower, 1 Sky Plaza Road
Hong Kong International Airport
Lantau, Hong Kong

Attn: Mr. Lawrence Tsui, Principal Manager, Environmental Compliance

14 March 2022

Dear Sir,

Contract No. 3102
3RS Independent Environmental Checker Consultancy Services

Submission of Monthly EM&A Report No. 74 (February 2022)

Reference is made to the Environmental Team's submission of the Monthly EM&A Report No. 74 under Condition 3.5 of the Environmental Permit No. EP-489/2014 certified by the ET Leader on 14 March 2022.

We write to verify the captioned submission in accordance with the requirement stipulated in Condition 3.5 of EP-489/2014.

Should you have any query, please feel free to contact the undersigned at 3922 9376.

Yours faithfully,
AECOM Asia Co. Ltd.

Jackel Law
Independent Environmental Checker

Contents

Abbreviations	1
Executive summary	3
1 Introduction	8
1.1 Background	8
1.2 Scope of this Report	8
1.3 Project Organisation	8
1.4 Summary of Construction Works	9
1.5 Summary of EM&A Programme Requirements	9
2 Air Quality Monitoring	12
2.1 Action and Limit Levels	12
2.2 Monitoring Equipment	12
2.3 Monitoring Methodology	12
2.3.1 Measuring Procedure	12
2.3.2 Maintenance and Calibration	13
2.4 Summary of Monitoring Results	13
2.5 Conclusion	13
3 Noise Monitoring	14
3.1 Action and Limit Levels	14
3.2 Monitoring Equipment	14
3.3 Monitoring Methodology	15
3.3.1 Monitoring Procedure	15
3.3.2 Maintenance and Calibration	15
3.4 Summary of Monitoring Results	15
3.5 Conclusion	16
4 Water Quality Monitoring	17
4.1 Action and Limit Levels	18
4.2 Monitoring Equipment	19
4.3 Monitoring Methodology	19
4.3.1 Measuring Procedure	19
4.3.2 Maintenance and Calibration	20
4.3.3 Laboratory Measurement / Analysis	20
4.4 Summary of Monitoring Results	20
4.5 Conclusion	21
5 Waste Management	22
5.1 Action and Limit Levels	22

5.2	Waste Management Status	22
5.3	Marine Sediment Management	23
6	Chinese White Dolphin Monitoring	24
6.1	Action and Limit Levels	24
6.2	CWD Monitoring Transects and Stations	24
6.2.1	Small Vessel Line-transect Survey	24
6.2.2	Land-based Theodolite Tracking Survey	26
6.3	CWD Monitoring Methodology	26
6.3.1	Small Vessel Line-transect Survey	26
6.3.2	Photo Identification	27
6.3.3	Land-based Theodolite Tracking Survey	27
6.4	Monitoring Results and Observations	28
6.4.1	Small Vessel Line-transect Survey	28
6.4.2	Photo Identification	31
6.4.3	Land-based Theodolite Tracking Survey	31
6.5	Progress Update on Passive Acoustic Monitoring	32
6.6	Site Audit for CWD-related Mitigation Measures	33
6.7	Timing of reporting CWD Monitoring Results	33
6.8	Summary of CWD Monitoring	33
7	Environmental Site Inspection and Audit	34
7.1	Environmental Site Inspection	34
7.2	Landscape and Visual Mitigation Measures	34
7.3	Land Contamination Assessment	41
7.4	Audit of SkyPier High Speed Ferries	42
7.5	Audit of Construction and Associated Vessels	42
7.6	Implementation of Dolphin Exclusion Zone	43
7.7	Status of Submissions under Environmental Permits	43
7.8	Compliance with Other Statutory Environmental Requirements	44
7.9	Analysis and Interpretation of Complaints, Notification of Summons and Status of Prosecutions	44
7.9.1	Complaints	44
7.9.2	Notifications of Summons or Status of Prosecution	44
7.9.3	Cumulative Statistics	44
8	Future Key Issues and Other EIA & EM&A Issues	45
8.1	Construction Programme for the Coming Reporting Period	45
8.2	Key Environmental Issues for the Coming Reporting Period	47
8.3	Monitoring Schedule for the Coming Reporting Period	47
8.4	Review of the Key Assumptions Adopted in the EIA Report	48
9	Conclusion and Recommendation	49

Tables

Table 1.1: Summary of Status of All Environmental Aspects under the Updated EM&A Manual	9
Table 2.1: Locations of Impact Air Quality Monitoring Stations	12
Table 2.2: Action and Limit Levels of Air Quality Monitoring	12
Table 2.3: Air Quality Monitoring Equipment	12
Table 2.4: Summary of Air Quality Monitoring Results	13
Table 3.1: Locations of Impact Noise Monitoring Stations	14
Table 3.2: Action and Limit Levels for Noise Monitoring	14
Table 3.3: Noise Monitoring Equipment	15
Table 3.4: Summary of Construction Noise Monitoring Results	16
Table 4.1: Monitoring Locations of Impact Water Quality Monitoring	17
Table 4.2: Action and Limit Levels for General Water Quality Monitoring and Regular DCM Monitoring	18
Table 4.3: The Control and Impact Stations during Flood Tide and Ebb Tide for General Water Quality Monitoring and Regular DCM Monitoring	19
Table 4.4: Water Quality Monitoring Equipment	19
Table 4.5: Other Monitoring Equipment	19
Table 4.6: Laboratory Measurement/ Analysis of SS and Heavy Metals	20
Table 5.1: Action and Limit Levels for Construction Waste	22
Table 5.2: Construction Waste Statistics	23
Table 6.1: Derived Values of Action and Limit Levels for Chinese White Dolphin Monitoring	24
Table 6.2: Coordinates of Transect Lines in NEL, NWL, AW, WL and SWL Survey Areas	25
Table 6.3: Land-based Theodolite Survey Station Details	26
Table 6.4: Comparison of CWD Encounter Rates of the Whole Survey Area with Action Levels	30
Table 6.5: Summary of Photo Identification	31
Table 6.6: Summary of Survey Effort and CWD Group of Land-based Theodolite Tracking	31
Table 7.1: Landscape and Visual – Construction Phase Audit Summary	35
Table 7.2: Examples of Landscape and Visual Mitigation Measures in the Reporting Period	36
Table 7.3: Monitoring Programme for Landscape and Visual	37
Table 7.4: Event and Action Plan for Landscape and Visual	37
Table 7.5: Summary of the Number of Retained, Transplanted and To-be-transplanted Trees in the Reporting Period	38
Table 7.6: Summary of the Transplanted Trees Updated in the Reporting Period	39
Table 7.7: Photos of the Existing Transplanted Trees Inspected in this Reporting Month	41
Table 7.8: Summary of Key Audit Findings against the SkyPier Plan	42
Table 7.9: Status of Submissions under Environmental Permit	43

Figures

- Figure 1.1 Locations of Key Construction Activities
- Figure 2.1 Locations of Air and Noise Monitoring Stations and Chek Lap Kok Wind Station
- Figure 4.1 Water Quality Monitoring Stations
- Figure 6.1 Vessel based Dolphin Monitoring Transects in Construction, Post-construction and Operation Phases
- Figure 6.2 Land based Dolphin Monitoring in Baseline and Construction Phases
- Figure 6.3 Sightings Distribution of Chinese White Dolphins
- Figure 6.4 Plots of First Sightings of All CWD Groups obtained from Land-based Stations
- Figure 6.5 Location for Autonomous Passive Acoustic Monitoring

Appendices

- Appendix A Environmental Mitigation Implementation Schedule (EMIS) for Construction Phase
- Appendix B Monitoring Schedule
- Appendix C Monitoring Results
- Appendix D Status of Environmental Permits and Licences
- Appendix E Cumulative Statistics on Exceedances, Environmental Complaints, Notification of Summons and Status of Prosecutions

Abbreviations

3RS	Three-Runway System
AAHK	Airport Authority Hong Kong
AECOM	AECOM Asia Company Limited
AFCD	Agriculture, Fisheries and Conservation Department
AIS	Automatic Information System
ANI	Encounter Rate of Number of Dolphins
APM	Automated People Mover
AW	Airport West
BHS	Baggage Handling System
C&D	Construction and Demolition
CAP	Contamination Assessment Plan
CAR	Contamination Assessment Report
CTCC	Construction Traffic Control Centre
CWD	Chinese White Dolphin
DCM	Deep Cement Mixing
DEZ	Dolphin Exclusion Zone
DO	Dissolved Oxygen
EIA	Environmental Impact Assessment
EM&A	Environmental Monitoring & Audit
EP	Environmental Permit
EPD	Environmental Protection Department
EPSS	Emergency Power Supply Systems
ET	Environmental Team
FCZ	Fish Culture Zone
HKBCF	Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities
HKIA	Hong Kong International Airport
HOKLAS	Hong Kong Laboratory Accreditation Scheme
HSF	High Speed Ferry
HVS	High Volume Sampler
IEC	Independent Environmental Checker
LKC	Lung Kwu Chau
MMHK	Mott MacDonald Hong Kong Limited
MMWP	Marine Mammal Watching Plan
MSS	Maritime Surveillance System
MTRMP-CAV	Marine Travel Routes and Management Plan for Construction and Associated Vessel
NEL	Northeast Lantau
NWL	Northwest Lantau
PAM	Passive Acoustic Monitoring
PM	Project Manager
SC	Sha Chau
SCZ	Speed Control Zone
SCLKCMP	Sha Chau and Lung Kwu Chau Marine Park
SS	Suspended Solids
SSSI	Site of Special Scientific Interest
STG	Encounter Rate of Number of Dolphin Sightings

SWL	Southwest Lantau
T2	Terminal 2
The Project	The Expansion of Hong Kong International Airport into a Three-Runway System
The SkyPier Plan	Marine Travel Routes and Management Plan for High Speed Ferries of SkyPier
The Manual	The Updated EM&A Manual
TSP	Total Suspended Particulates
WL	West Lantau
WMP	Waste Management Plan

Executive summary

The “Expansion of Hong Kong International Airport into a Three-Runway System” (the Project) serves to meet the future air traffic demands at Hong Kong International Airport (HKIA). On 7 November 2014, the Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-185/2014) for the Project was approved and an Environmental Permit (EP) (Permit No.: EP-489/2014) was issued for the construction and operation of the Project.

Airport Authority Hong Kong (AAHK) commissioned Mott MacDonald Hong Kong Limited (MMHK) to undertake the role of Environmental Team (ET) for carrying out the Environmental Monitoring & Audit (EM&A) works during the construction phase of the Project in accordance with the Updated EM&A Manual (the Manual).

This is the 74th Construction Phase Monthly EM&A Report for the Project which summarises the monitoring results and audit findings of the EM&A programme during the reporting period from 1 to 28 February 2022.

Key Activities in the Reporting Period

The key activities of the Project carried out in the reporting period are located in reclamation areas and existing airport island respectively. Works in the reclamation areas included seawall construction, filling and ground improvement works, together with runway, concourse and associated works. Land-based works on existing airport island involved mainly airfield works, Terminal 2 expansion works, modification and tunnel work for Automated People Mover (APM) and Baggage Handling System (BHS), and preparation work for utilities, with activities include road and drainage works, cable ducting, demolition, piling, and excavation works.



EM&A Activities Conducted in the Reporting Period

The monthly EM&A programme was undertaken in accordance with the Manual of the Project. Summary of the monitoring activities during this reporting period is presented as below:

Monitoring Activities	Number of Sessions
1-hour Total Suspended Particulates (TSP) air quality monitoring	24
Noise monitoring	14
Water quality monitoring	11
Vessel line-transect surveys for Chinese White Dolphin (CWD) monitoring	2
Land-based theodolite tracking survey effort for CWD monitoring	2

Environmental auditing works, including weekly site inspections of construction works conducted by the ET and bi-weekly site inspections conducted by the Independent Environmental Checker (IEC), audit of SkyPier High Speed Ferries (HSF), audit of construction and associated vessels, and audit of implementation of Marine Mammal Watching Plan (MMWP) and Dolphin Exclusion Zone (DEZ) Plan, were conducted in the reporting period. Due to the COVID-19 pandemic, virtual and physical site inspections of construction works to audit the implementation of proper environmental pollution control and mitigation measures for the Project were conducted by ET and IEC in this reporting period on a weekly and bi-weekly basis, respectively. Based on the information including ET’s observations, records of Maritime Surveillance System (MSS), and contractors’ site records, it is noted that environmental pollution control and mitigation measures were properly implemented and construction activities of the Project in the reporting period did not introduce adverse impacts to the sensitive receivers.

Snapshots of EM&A Activities in the Reporting Period

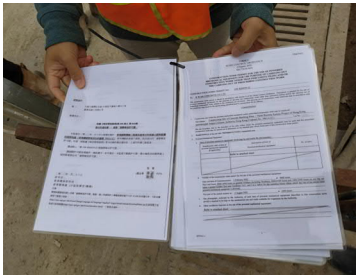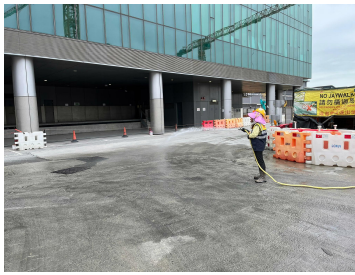		
Impact Air Quality Monitoring conducted by ET in Man Tung Road Park	On-site Checking of Construction Noise Permit conducted by ET	Dust Suppression Measure conducted by Contractor

Results of Impact Monitoring

The monitoring works for construction dust, construction noise, water quality, construction waste, landscape & visual, and CWD were conducted during the reporting period in accordance with the Manual.

Monitoring results of construction dust, construction noise, water quality, and CWD did not trigger the corresponding Action and Limit Levels in the reporting period.

For waste management, a complaint regarding general refuse was received in this reporting period. This complaint triggered the relevant Action Level, and the corresponding investigation was subsequently conducted in accordance with the Manual and the Complaint Management Plan of the Project. To conclude, follow-up actions have been made by ET and the related contractor, and the case was considered closed.

Summary of Upcoming Key Issues

Reclamation Works:

Contract 3206 Main Reclamation Works

- Seawall construction; and
- Backfilling works.

Airfield Works

Contract 3301 North Runway Crossover Taxiway

- Cabling works; and
- Stockpiling.

Contract 3302 Eastern Vehicular Tunnel Advance Works

- Construction of tunnel structure;
- Pipe and drainage diversion works;
- Excavation and lateral support systems installation; and
- Stockpiling.

Contract 3303 Third Runway and Associated Works

- Architectural, Builder's and Finishing works;
- Footing and utilities work;
- Box culvert construction;
- Piling work;
- Operation of asphalt plant; and

- Cable laying and ducting works.

Contract 3305 Airfield Ground Lighting System

- Cabling works;
- Network installation; and
- Genset installation.

Contract 3306 Observation Facility Control System Supporting Interim 2RS and 3RS

- Equipment installation; and
- Installation of temporary site accommodation.

Contract 3307 Fire Training Facility

- Architectural, Builder's and Finishing works;
- Drainage and utilities works; and
- Building construction.

Contract 3308 Foreign Object Debris Detection System

- Foreign Object Debris Tower installation.

Contract 3310 North Runway Modification Works

- Excavation;
- Cutter soil mixing; and
- Deep cement mixing.

Third Runway Concourse:

Contract 3403 New Integrated Airport Centres Building and Civil Works

- Architectural, Builder's Work and Finishing works;
- Road works;
- Cabling works; and
- Underground utilities construction.

Contract 3404 Integrated Airport Control System

- Equipment installation; and
- Cable laying.

Contract 3405 Third Runway Concourse Foundation and Substructure Works

- Sheet piling and bored piling;
- Excavation; and
- Road formation.

Contract 3408 Third Runway Concourse and Apron Works

- Site setup works; and
- Excavation and lateral support works.

Terminal 2 Expansion:

Contract 3508 Terminal 2 Expansion Works

- Excavation and footing construction;
- Bridge demolition;
- Block wall construction;
- Drainage works;
- Temporary road construction;
- TBM mobilization; and
- Architectural, Builder's Work and Finishing works.

Automated People Mover (APM) and Baggage Handling System (BHS):

Contract 3601 New Automated People Mover System (TRC Line)

- Guidebeam installation.

Contract 3602 Existing APM System Modification Works

- Car modification; and
- Concrete plinth and stitch construction.

Contract 3603 Baggage Handling System (BHS)

- BHS installation.

Construction Support (Facilities):

Contract 3721 Construction Support Infrastructure Works

- Laying of drainage pipes and ducts;
- Site clearance;
- Paving works; and
- Road works.

Contract 3723 Construction Support Facilities

- Clearance works;
- RC works; and
- Finishing works.

Airport Support Infrastructure:

Contract 3801 APM and BHS Tunnels on Existing Airport Island

- Excavation;
- Box jacking operation;
- Mass concreting; and
- Ventilation ducts construction.

Contract 3802 APM and BHS Tunnels and Related Works

- Fencing erection;
- Installation of dewatering well; and
- Excavation and lateral supports.

Construction Support (Services / Licences):

Contract 3901A Concrete Batching Facility

- Operation of concrete batching plant; and
- Operation of conveyor belt.

Contract 3901B Concrete Batching Facility

- Operation of concrete batching plant; and
- Testing and commissioning for conveyor belt.

Summary Table

The following table summarises the key findings of the EM&A programme during the reporting period:

	Yes	No	Details	Analysis / Recommendation / Remedial Actions
Breach of Limit Level [^]		√	No breach of Limit Level was recorded.	Nil
Breach of Action Level [^]	√		For waste management, a complaint regarding general refuse was received in this reporting period. This complaint triggered the relevant Action Level, and the corresponding investigation was subsequently conducted in accordance with the Manual and the Complaint Management Plan of the Project.	Follow-up actions have been made by ET and the related contractor, and the case was considered closed.
Complaint Received	√		A complaint regarding suspected dump truck for garbage disposal that was not properly covered was received on 18 February 2022.	ET requested the relevant contractor to provide information related to the complaint. No item related to the covering of dump trucks was recorded during regular site inspections. During an ad-hoc inspection, some dump trucks were observed not fully covered when leaving the construction site onto RoRo barges in which ET immediately followed up with the contractor. All 3RS contractors were reminded to ensure the proper covering of dump trucks for garbage disposal and avoid potential blowing away of materials during the process. Hence, the case was considered closed.
Notification of any summons and status of prosecutions		√	No notification of summons nor prosecution was received.	Nil
Change that affect the EM&A		√	There was no change to the construction works that may affect the EM&A.	Nil

Note:

[^] Only triggering of Action or Limit Level found related to Project works is counted as Breach of Action or Limit Level.

1 Introduction

1.1 Background

On 7 November 2014, the Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-185/2014) for the “Expansion of Hong Kong International Airport into a Three-Runway System” (the Project) was approved and an Environmental Permit (EP) (Permit No.: EP-489/2014) was issued for the construction and operation of the Project.

Airport Authority Hong Kong (AAHK) commissioned Mott MacDonald Hong Kong Limited (MMHK) to undertake the role of Environmental Team (ET) for carrying out the Environmental Monitoring & Audit (EM&A) works during the construction phase of the Project in accordance with the Updated EM&A Manual (the Manual) submitted under EP Condition 3.1¹. AECOM Asia Company Limited (AECOM) was employed by AAHK as the Independent Environmental Checker (IEC) for the Project.

The Project covers the expansion of the existing airport into a three-runway system (3RS) with key project components comprising land formation of about 650 ha and all associated facilities and infrastructure including taxiways, aprons, aircraft stands, a passenger concourse, an expanded Terminal 2, all related airside and landside works and associated ancillary and supporting facilities. The submarine aviation fuel pipelines and submarine power cables also require diversion as part of the works.

Construction of the Project is to proceed in the general order of diversion of the submarine aviation fuel pipelines, diversion of the submarine power cables, land formation, and construction of infrastructure, followed by construction of superstructures.

The summary of construction works programme can be referred to **Section 1.4**.

1.2 Scope of this Report

This is the 74th Construction Phase Monthly EM&A Report for the Project which summarises the key findings of the EM&A programme during the reporting period from 1 to 28 February 2022.

1.3 Project Organisation

The Project’s organisation structure presented in Appendix B of the Construction Phase Monthly EM&A Report No.1 remained unchanged during the reporting period. Contact details of the key personnel presented in Section 1.3 of the Construction Phase Monthly EM&A Report No.73 remained unchanged during the reporting period.

¹ The Manual is available on the Project’s dedicated website (accessible at: <http://env.threerunwaysystem.com/en/index.html>).

1.4 Summary of Construction Works

The key activities of the Project carried out in the reporting period are located in reclamation areas and existing airport island respectively. Works in the reclamation areas included seawall construction, filling and ground improvement works, together with runway, concourse and associated works. Land-based works on existing airport island involved mainly airfield works, Terminal 2 expansion works, modification and tunnel work for Automated People Mover (APM) and Baggage Handling System (BHS), and preparation work for utilities, with activities include road and drainage works, cable ducting, demolition, piling, and excavation works.

The locations of key construction activities are presented in **Figure 1.1**.

1.5 Summary of EM&A Programme Requirements

The status for all environmental aspects are presented in **Table 1.1**. The EM&A requirements remained unchanged during the reporting period.

Table 1.1: Summary of Status of All Environmental Aspects under the Updated EM&A Manual

Parameters	EM&A Requirements	Status
Air Quality		
Baseline Monitoring	At least 14 consecutive days before commencement of construction work	The baseline air quality monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4.
Impact Monitoring	At least 3 times every 6 days	On-going
Noise		
Baseline Monitoring	Daily for a period of at least two weeks prior to the commencement of construction works	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4.
Impact Monitoring	Weekly	On-going
Water Quality		
General Baseline Water Quality Monitoring for reclamation, water jetting and field joint works	Three days per week, at mid-flood and mid-ebb tides, for at least four weeks prior to the commencement of marine works.	The baseline water quality monitoring result has been reported in Baseline Water Quality Monitoring Report and submitted to EPD under EP Condition 3.4.
General Impact Water Quality Monitoring for reclamation, water jetting and field joint works	Three days per week, at mid-flood and mid-ebb tides.	On-going for reclamation works. General impact water quality monitoring for water jetting works was completed on 23 May 2017.
Initial Intensive Deep Cement Mixing (DCM) Water Quality Monitoring	At least four weeks	The Initial Intensive DCM Monitoring Report was submitted and approved by EPD in accordance with the Detailed Plan on DCM.
Regular DCM Water Quality Monitoring	Three times per week until completion of DCM works.	On-going
Sewerage and Sewage Treatment		
Methodology for carrying out annual sewage flow monitoring for concerned gravity sewer	Methodology to be prepared and submitted to EPD one year before the scheduled commencement of operation of the proposed third runway	The proposed methodology of the annual sewage flow monitoring was approved by EPD. The annual flow monitoring has been started since June 2021.
Details of the routine H ₂ S monitoring system for the sewerage system of 3RS	Details to be prepared and submitted to EPD at least one year before commencement of the operation of 3RS	The details of the routine H ₂ S monitoring system will be prepared and submitted to EPD at least one year before commencement of operation of 3RS.
Waste Management		

Parameters	EM&A Requirements	Status
Waste Monitoring	At least weekly	On-going
Land Contamination		
Supplementary Contamination Assessment Plan (CAP)	At least 3 months before commencement of any soil remediation works.	The Supplementary CAP was submitted and approved by EPD under EP Condition 2.20.
Contamination Assessment Report (CAR) for Golf Course	CAR to be submitted for golf course	The CAR for Golf Course was submitted and accepted by EPD.
Contamination Assessment Reports (CAR) for Terminal 2 Emergency Power Supply Systems	CAR to be submitted for Terminal 2 Emergency Power Supply Systems	The CARs for Terminal 2 Emergency Power Supply Systems were submitted and accepted by EPD.
Terrestrial Ecology		
Pre-construction Egretty Survey Plan	Once per month in the breeding season between April and July, prior to the commencement of HDD drilling works.	The Egretty Survey Plan was submitted and approved by EPD under EP Condition 2.14.
Ecological Monitoring	Monthly monitoring during the HDD construction works period from August to March.	The terrestrial ecological monitoring at Sheung Sha Chau was completed in January 2019.
Marine Ecology		
Pre-Construction Phase Coral Dive Survey	Prior to marine construction works	The Coral Translocation Plan was submitted and approved by EPD under EP Condition 2.12.
Coral Translocation	-	The coral translocation was completed.
Post-Translocation Coral Monitoring	As per an enhanced monitoring programme based on the Coral Translocation Plan	The post-translocation monitoring programme according to the Coral Translocation Plan was completed in April 2018.
Chinese White Dolphins (CWD)		
Baseline Monitoring	6 months of baseline surveys before the commencement of land formation related construction works. Vessel line transect surveys: Two full surveys per month; Land-based theodolite tracking surveys: Two days per month at the Sha Chau station and two days per month at the Lung Kwu Chau station; and Passive Acoustic Monitoring (PAM): For the whole duration of baseline period.	Baseline CWD results were reported in the CWD Baseline Monitoring Report and submitted to EPD in accordance with EP Condition 3.4.
Impact Monitoring	Vessel line transect surveys: Two full surveys per month; Land-based theodolite tracking surveys: One day per month at the Sha Chau station and one day per month at the Lung Kwu Chau station; and PAM: For the whole duration for land formation related construction works.	On-going
Landscape & Visual		
Landscape & Visual Plan	At least 3 months before the commencement of construction works on the formed land of the Project.	The Landscape & Visual Plan was submitted and approved by EPD under EP Condition 2.18
Baseline Monitoring	One-off survey within the Project site boundary prior to commencement of any construction works	The baseline landscape & visual monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4.
Impact Monitoring	Weekly	On-going
Environmental Auditing		

Parameters	EM&A Requirements	Status
Regular site inspection	Weekly	On-going
Marine Mammal Watching Plan (MMWP) implementation measures	Monitor and check	On-going
Dolphin Exclusion Zone (DEZ) Plan implementation measures	Monitor and check	On-going
SkyPier High Speed Ferries (HSF) implementation measures	Monitor and check	On-going
Construction and Associated Vessels Implementation measures	Monitor and check	On-going
Silt Curtain Deployment Plan implementation measures	Monitor and check	On-going
Spill Response Plan implementation measures	Monitor and check	On-going
Complaint Hotline and Email channel	Construction phase	On-going
Environmental Log Book	Construction phase	On-going

Taking into account the construction works in this reporting period, impact monitoring of air quality, noise, water quality, waste management, landscape & visual, and CWD were carried out in the reporting period.

The EM&A programme also involved weekly site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report. Due to the COVID-19 pandemic, virtual and physical site inspections of construction works to audit the implementation of proper environmental pollution control and mitigation measures for the Project were conducted by ET and IEC on a weekly and bi-weekly basis, respectively. To promote the environmental awareness and enhance the environmental performance of the contractors, regular environmental management meetings were conducted during the reporting period, which are summarised as below:

- Eighteen environmental management meetings for EM&A review with works contracts: 4, 10, 15, 16, 17, 22, 23, 24 and 28 February 2022.

The EM&A programme has been following the recommendations presented in the approved EIA Report and the Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix A**.

2 Air Quality Monitoring

Air quality monitoring of 1-hour Total Suspended Particulates (TSP) was conducted three times every six days at two representative monitoring stations in the vicinity of air sensitive receivers in Tung Chung and villages in North Lantau in accordance with the Manual. **Table 2.1** describes the details of the monitoring stations. **Figure 2.1** shows the locations of the monitoring stations.

Table 2.1: Locations of Impact Air Quality Monitoring Stations

Monitoring Station	Location
AR1A	Man Tung Road Park
AR2	Village House at Tin Sum

2.1 Action and Limit Levels

In accordance with the Manual, baseline air quality monitoring of 1-hour TSP levels at the two air quality monitoring stations were established as presented in the Baseline Monitoring Report. The Action and Limit Levels of the air quality monitoring stipulated in the EM&A programme for triggering the relevant investigation and follow-up procedures under the programme are provided in **Table 2.2**.

Table 2.2: Action and Limit Levels of Air Quality Monitoring

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AR1A	306	500
AR2	298	

2.2 Monitoring Equipment

Portable direct reading dust meter was used to carry out the air quality monitoring. Details of equipment used in the reporting period are given in **Table 2.3**.

Table 2.3: Air Quality Monitoring Equipment

Equipment	Brand and Model	Last Calibration Date	Calibration Certificate Provided in
Portable direct reading dust meter (Laser dust monitor)	SIBATA LD-3B-2 (Serial No. 296098)	20 Oct 2021	Monthly EM&A Report No. 70, Appendix E
	SIBATA LD-3B-1 (Serial No. 597337)	10 May 2021	Monthly EM&A Report No. 65, Appendix D

2.3 Monitoring Methodology

2.3.1 Measuring Procedure

The measurement procedures involved in the impact air quality monitoring can be summarised as follows:

- The portable direct reading dust meter was mounted on a tripod at a height of 1.2m above the ground.
- Prior to the measurement, the equipment was set up for 1 minute span check and 6 second background check.

- c. The one hour dust measurement was started. Site conditions and dust sources at the nearby area were recorded on a record sheet.
- d. When the measurement completed, the “Count” reading per hour was recorded for result calculation.

2.3.2 Maintenance and Calibration

The portable direct reading dust meter is calibrated every year against high volume sampler (HVS) to check the validity and accuracy of the results measured by direct reading method. The calibration record of the HVS provided in Appendix D of Construction Phase Monthly EM&A Report No. 65, and the calibration certificates of portable direct reading dust meters listed in **Table 2.3** are valid in the reporting period.

2.4 Summary of Monitoring Results

The air quality monitoring schedule involved in the reporting period is provided in **Appendix B**.

The air quality monitoring results in the reporting period are summarised in **Table 2.4**. Detailed impact monitoring results are presented in **Appendix C**.

Table 2.4: Summary of Air Quality Monitoring Results

Monitoring Station	1-hr TSP Concentration Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AR1A	21 - 124	306	500
AR2	19 - 105	298	

The monitoring results were within the corresponding Action and Limit Levels at all monitoring stations in the reporting period.

General meteorological conditions throughout the impact monitoring period were recorded. Wind data including wind speed and wind direction for each monitoring day were collected from the Chek Lap Kok Wind Station.

2.5 Conclusion

No dust emission source was observed at the monitoring stations during the monitoring sessions. As the sensitive receivers were far away from the construction activities, with the implementation of dust control measures, there was no adverse impact at the sensitive receivers attributable to the works of the Project.

3 Noise Monitoring

Noise monitoring in the form of 30-minute measurements of L_{eq} , L_{10} , and L_{90} levels was conducted once per week between 0700 and 1900 on normal weekdays at four representative monitoring stations in the vicinity of noise sensitive receivers in Tung Chung and villages in North Lantau in accordance with the Manual. **Table 3.1** describes the details of the monitoring stations. **Figure 2.1** shows the locations of the monitoring stations.

Table 3.1: Locations of Impact Noise Monitoring Stations

Monitoring Station	Location	Type of measurement
NM1A	Man Tung Road Park	Free field
NM2 ⁽¹⁾	Tung Chung West Development	To be determined
NM3A ⁽²⁾	Site Office	Facade
NM4	Ching Chung Hau Po Woon Primary School	Free field
NM5	Village House in Tin Sum	Free field
NM6	House No. 1, Sha Lo Wan	Free field

Note:

- (1) As described in Section 4.3.3 of the Manual, noise monitoring at NM2 will only commence after occupation of the future Tung Chung West Development.
- (2) According to Section 4.3.3 of the Manual, the noise monitoring at NM3A was temporarily suspended starting from 1 September 2018 and would be resumed with the completion of the Tung Chung East Development.

3.1 Action and Limit Levels

In accordance with the Manual, baseline noise levels at the noise monitoring stations were established as presented in the Baseline Monitoring Report. The Action and Limit Levels of the noise monitoring stipulated in the EM&A programme for triggering the relevant investigation and follow-up procedures under the programme are provided in **Table 3.2**.

Table 3.2: Action and Limit Levels for Noise Monitoring

Monitoring Stations	Time Period	Action Level	Limit Level, $L_{eq}(30mins)$ dB(A)
NM1A, NM2, NM3A, NM4, NM5 and NM6	0700-1900 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75dB(A) ⁽¹⁾

Note:

- (1) The Limit Level for NM4 is reduced to 70dB(A) for being an educational institution. During school examination period, the Limit Level is further reduced to 65dB(A).

3.2 Monitoring Equipment

Noise monitoring was performed using sound level meter at each designated monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was used to check the sound level meters by a known sound pressure level for field measurement. Details of equipment used in the reporting period are given in **Table 3.3**.

Table 3.3: Noise Monitoring Equipment

Equipment	Brand and Model	Last Calibration Date	Calibration Certificate Provided in
Integrated Sound Level Meter	Rion NL-52 (Serial No. 00998505)	20 Mar 2021	Monthly EM&A Report No. 63, Appendix E
	Rion NL-52 (Serial No. 01287679)	20 Jun 2021	Monthly EM&A Report No. 66, Appendix D
Acoustic Calibrator	Casella CEL-120/1 (Serial No. 2383737)	20 Jun 2021	Monthly EM&A Report No. 66, Appendix D
	Castle GA607 (Serial No. 040162)	20 Mar 2021	Monthly EM&A Report No. 63, Appendix E

3.3 Monitoring Methodology

3.3.1 Monitoring Procedure

The monitoring procedures involved in the noise monitoring can be summarised as follows:

- The sound level meter was set on a tripod at least a height of 1.2m above the ground for free-field measurements at monitoring stations NM1A, NM4, NM5 and NM6. A correction of +3dB(A) was applied to the free field measurements.
- Façade measurements were made at the monitoring station NM3A.
- Parameters such as frequency weighting, time weighting and measurement time were set.
- Prior to and after each noise measurement, the meter was calibrated using the acoustic calibrator. If the difference in the calibration level before and after measurement was more than 1dB(A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- During the monitoring period, L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a record sheet.
- Noise measurement results, when higher than the baseline monitoring levels, were corrected with reference to the baseline monitoring levels.
- Observations were recorded when high intrusive noise (e.g. dog barking, helicopter noise) was observed during the monitoring.

3.3.2 Maintenance and Calibration

The maintenance and calibration procedures are summarised below:

- The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
- The meter and calibrator were sent to the supplier or laboratory accredited under Hong Kong Laboratory Accreditation Scheme (HOKLAS) to check and calibrate at yearly intervals.

Calibration certificates of the sound level meters and acoustic calibrators used in the noise monitoring listed in **Table 3.3** are valid in the reporting period.

3.4 Summary of Monitoring Results

The noise monitoring schedule involved in the reporting period is provided in **Appendix B**.

The noise monitoring results in the reporting period are summarised in **Table 3.4**. Detailed impact monitoring results are presented in **Appendix C**.

Table 3.4: Summary of Construction Noise Monitoring Results

Monitoring Station	Noise Level Range, dB(A)	Limit Level, dB(A)
	<i>L_{eq}</i> (30mins)	<i>L_{eq}</i> (30mins)
NM1A ⁽¹⁾	57 - 61	75
NM4 ⁽¹⁾	60 - 62	70 ⁽²⁾
NM5 ⁽¹⁾⁽³⁾	53 - 58	75
NM6 ⁽¹⁾⁽³⁾	62 - 68	75

Notes:

- (1) +3dB(A) Façade correction included;
- (2) Reduced to 65dB(A) during school examination periods at NM4. No school examination took place during this reporting period.
- (3) Some of the noise measurement results were higher than the baseline monitoring levels. In order to reduce the influence of non-Project related noise on the monitoring results, these measurement results were corrected with reference to the baseline monitoring levels.

No complaints were received from any sensitive receiver that triggered the Action Level. All monitoring results were also within the corresponding Limit Levels at all monitoring stations in the reporting period.

3.5 Conclusion

As the construction activities were far away from the monitoring stations, major sources of noise dominating the monitoring stations observed during the construction noise impact monitoring were traffic noise near NM1A and aircraft noise near NM6 during this reporting period. It is considered that the monitoring work during the reporting period was effective and there was no adverse impact attributable to the Project activities.

4 Water Quality Monitoring

Water quality monitoring of DO, pH, temperature, salinity, turbidity, suspended solids (SS), total alkalinity, chromium, and nickel was conducted three days per week, at mid-ebb and mid-flood tides, at a total of 14 water quality monitoring stations, comprising 6 impact (IM) stations, 5 sensitive receiver (SR) stations and 3 control (C) stations in the vicinity of water quality sensitive receivers around the airport island in accordance with the Manual. The purpose of water quality monitoring at the IM stations is to promptly capture any potential water quality impact from the Project before it could become apparent at sensitive receivers (represented by the SR stations). **Table 4.1** describes the details of the monitoring stations. **Figure 4.1** shows the locations of the monitoring stations.

Table 4.1: Monitoring Locations of Impact Water Quality Monitoring

Monitoring Station	Description	Coordinates		Parameters
		Easting	Northing	
C1	Control Station	804247	815620	<u>General Parameters</u> DO, pH, Temperature, Salinity, Turbidity, SS
C2	Control Station	806945	825682	
C3 ⁽³⁾	Control Station	817803	822109	
IM1 ⁽⁷⁾	Impact Station	806458	818351	
IM2 ⁽⁷⁾	Impact Station	806236	819183	<u>DCM Parameters</u> Total Alkalinity, Heavy Metals ⁽²⁾
IM7 ⁽⁷⁾	Impact Station	806835	821349	
IM10 ⁽⁷⁾	Impact Station	809838	822240	
IM11 ⁽⁷⁾	Impact Station	810545	821501	
IM12 ⁽⁷⁾	Impact Station	811519	821162	<u>General Parameters</u> DO, pH, Temperature, Salinity, Turbidity, SS
SR1A ⁽¹⁾	Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities (HKBCF) Seawater Intake for cooling	812660	819977	
SR2	Planned marine park / hard corals at The Brothers / Tai Mo To	814166	821463	
SR3	Sha Chau and Lung Kwu Chau Marine Park / fishing and spawning grounds in North Lantau	807571	822147	
SR4A	Sha Lo Wan	807810	817189	<u>General Parameters</u> DO, pH, Temperature, Salinity, Turbidity, SS
SR8 ⁽⁶⁾	Seawater Intake for cooling at Hong Kong International Airport (East)	811623	820390	

Notes:

- (1) With the operation of HKBCF, water quality monitoring at SR1A station was commenced on 25 October 2018. To better reflect the water quality in the immediate vicinity of the intake, the monitoring location of SR1A has been shifted closer to the intake starting from 5 January 2019.

- (2) Details of selection criteria for the two heavy metals for regular DCM monitoring refer to the Detailed Plan on Deep Cement Mixing available on the dedicated 3RS website (<http://env.threerunwaysystem.com/en/ep-submissions.html>). DCM specific water quality monitoring parameters (total alkalinity and heavy metals) were only conducted at C1 to C3, SR2, and IM1 to IM12.
- (3) According to the Baseline Water Quality Monitoring Report, C3 station is not adequately representative as a control station of impact/ SR stations during the flood tide. The control reference has been changed from C3 to SR2 from 1 September 2016 onwards.
- (4) Total alkalinity and heavy metals results are collected at SR2 as a control station for regular DCM monitoring.
- (5) As the access to SR6 was obstructed by the construction activities and temporary structures for Tung Chung New Town Extension, the monitoring location has been relocated to SR6A starting from 8 August 2019.
- (6) The monitoring location for SR8 is subject to further changes due to silt curtain arrangements and the progressive relocation of this seawater intake.
- (7) With the seawall completion and removal of enhanced open sea silt curtains, these monitoring stations were relocated back to their original locations. For IM2, there was minor adjustment of the monitoring location.

4.1 Action and Limit Levels

In accordance with the Manual, baseline water quality levels at the representative water quality monitoring stations were established as presented in the Baseline Water Quality Monitoring Report. The Action and Limit Levels of general water quality monitoring and regular DCM monitoring stipulated in the EM&A programme for triggering the relevant investigation and follow-up procedures under the programme are provided in **Table 4.2**. The control and impact stations during ebb tide and flood tide for general water quality monitoring and regular DCM monitoring are presented in **Table 4.3**.

Table 4.2: Action and Limit Levels for General Water Quality Monitoring and Regular DCM Monitoring

Parameters		Action Level (AL)		Limit Level (LL)	
Action and Limit Levels for general water quality monitoring and regular DCM monitoring (excluding SR1A & SR8)					
General Water Quality Monitoring	DO in mg/l (Surface, Middle & Bottom)	Surface and Middle 4.5mg/l		Surface and Middle 4.1mg/l	
		Bottom 3.4mg/l		Bottom 2.7mg/l	
	Suspended Solids (SS) 23 in mg/l		or 120% of upstream control station at the same tide of the same day, whichever is higher	37	or 130% of upstream control station at the same tide of the same day, whichever is higher
	Turbidity in NTU	22.6		36.1	
Regular DCM Monitoring	Total Alkalinity in ppm	95		99	
	Representative Heavy Metals for regular DCM monitoring (Chromium) in µg/l	0.2		0.2	
	Representative Heavy Metals for regular DCM monitoring (Nickel) in µg/l	3.2		3.6	
Action and Limit Levels SR1A					
SS (mg/l))		33		42	
Action and Limit Levels SR8					
SS (mg/l)		52		60	

Notes:

- (1) For DO measurement, non-compliance occurs when monitoring result is lower than the limits.
- (2) For parameters other than DO, non-compliance of water quality results when monitoring results is higher than the limits.
- (3) Depth-averaged results are used unless specified otherwise.
- (4) Details of selection criteria for the two heavy metals for regular DCM monitoring refer to the Detailed Plan on Deep Cement Mixing available on the dedicated 3RS website (<http://env.threerunwaysystem.com/en/ep-submissions.html>)

- (5) The Action and Limit Levels for the two representative heavy metals chosen will be the same as that for the intensive DCM monitoring.

Table 4.3: The Control and Impact Stations during Flood Tide and Ebb Tide for General Water Quality Monitoring and Regular DCM Monitoring

Control Station	Impact Stations
Flood Tide	
C1	IM1, IM2, IM7, SR3
SR2 ⁽¹⁾	IM7, IM10, IM11, IM12, SR1A, SR3, SR4A, SR8
Ebb Tide	
C1	SR4A
C2	IM1, IM2, IM7, IM10, IM11, IM12, SR1A, SR2, SR3, SR8

Note:

- (1) As per findings of Baseline Water Quality Monitoring Report, the control reference has been changed from C3 to SR2 from 1 September 2016 onwards.

4.2 Monitoring Equipment

Table 4.4 summarises the equipment used in the reporting period for monitoring of specific water quality parameters under the water quality monitoring programme.

Table 4.4: Water Quality Monitoring Equipment

Equipment	Brand and Model	Last Calibration Date	Calibration Certificate Provided in
Multifunctional Meter (measurement of DO, pH, temperature, salinity and turbidity)	YSI ProDSS (Serial No. 21G105356)	24 Dec 2021	Monthly EM&A Report No. 72, Appendix D
	YSI ProDSS (Serial No. 16H104233) ⁽¹⁾	26 Nov 2021	Monthly EM&A Report No. 71, Appendix E
	YSI ProDSS (Serial No. 16H104234) ⁽¹⁾	26 Nov 2021	Monthly EM&A Report No. 71, Appendix E
	YSI ProDSS (Serial No. 17E100747)	24 Dec 2021	Monthly EM&A Report No. 72, Appendix D
Digital Titrator (measurement of total alkalinity)	Titrette Bottle-top Burette, 50ml (Serial No. 10N64701)	7 Jan 2022	Monthly EM&A Report No. 73, Appendix D

Note:

- (1) The monitoring equipment was not used in the reporting period after the expiry date of the calibration certificate (25 Feb 2022).

Other equipment used as part of the impact water quality monitoring programme are listed in **Table 4.5**.

Table 4.5: Other Monitoring Equipment

Equipment	Brand and Model
Water Sampler	Van Dorn Water Sampler
Positioning Device (measurement of GPS)	Garmin eTrex Vista HCx
Current Meter (measurement of current speed and direction, and water depth)	Sontek HydroSurveyor

4.3 Monitoring Methodology

4.3.1 Measuring Procedure

Water quality monitoring samples were taken at three depths (at 1m below surface, at mid-depth, and at 1m above bottom) for locations with water depth >6m. For locations with water depth

between 3m and 6m, water samples were taken at two depths (surface and bottom). For locations with water depth <3m, only the mid-depth was taken. Duplicate water samples were taken and analysed.

The water samples for all monitoring parameters were collected, stored, preserved and analysed according to the Standard Methods, APHA 22nd ed. and/or other methods as agreed by the EPD. In-situ measurements at monitoring locations including temperature, pH, DO, turbidity, salinity, alkalinity and water depth were collected by equipment listed in **Table 4.4** and **Table 4.5**. Water samples for heavy metals and SS analysis were stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen), delivered to the laboratory within 24 hours of collection.

4.3.2 Maintenance and Calibration

Calibration of In-situ Instruments

All in-situ monitoring instrument was checked, calibrated and certified by a laboratory accredited under HOKLAS before use. Responses of sensors and electrodes were checked with certified standard solutions before each use.

Wet bulb calibration for a DO meter was carried out before commencement of monitoring and after completion of all measurements each day. Calibration was not conducted at each monitoring location as daily calibration is adequate for the type of DO meter employed. A zero check in distilled water was performed with the turbidity probe at least once per monitoring day. The probe was then calibrated with a solution of known NTU. In addition, the turbidity probe was calibrated at least twice per month to establish the relationship between turbidity readings (in NTU) and levels of SS (in mg/l). Accuracy check of the digital titrator was performed at least once per monitoring day.

Calibration certificates of the monitoring equipment used in the reporting period are listed in **Table 4.4**.

4.3.3 Laboratory Measurement / Analysis

Analysis of SS and heavy metals have been carried out by a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (Reg. No. HOKLAS 066). Sufficient water samples were collected at all the monitoring stations for carrying out the laboratory SS and heavy metals determination. The SS and heavy metals determination works were started within 24 hours after collection of the water samples. The analysis of SS and heavy metals have followed the standard methods summarised in **Table 4.6**. The QA/QC procedures for laboratory measurement/ analysis of SS and heavy metals were presented in Appendix F of the Construction Phase Monthly EM&A Report No.8.

Table 4.6: Laboratory Measurement/ Analysis of SS and Heavy Metals

Parameters	Instrumentation	Analytical Method	Reporting Limit
SS	Analytical Balance	APHA 2540D	2mg/l
Heavy Metals			
Chromium (Cr)	ICP-MS	USEPA 6020A	0.2µg/l
Nickel (Ni)	ICP-MS	USEPA 6020A	0.2µg/l

4.4 Summary of Monitoring Results

The water quality monitoring schedule for the reporting period is updated and provided in **Appendix B**.

The water quality monitoring results for all parameters (i.e. DO, turbidity, SS, total alkalinity, chromium and nickel) obtained during the reporting period were within their corresponding Action and Limit Levels. The detailed monitoring results are presented in **Appendix C**.

4.5 Conclusion

During the reporting period, all monitoring results were within their corresponding Action and Limit Levels. Nevertheless, as part of the EM&A programme, the construction methods and mitigation measures for water quality will continue to be monitored and opportunities for further enhancement will continue to be explored and implemented where possible, to strive for better protection of water quality and the marine environment.

In the meantime, the contractors were reminded to implement and maintain all mitigation measures as recommended in the Manual during weekly site inspection and regular environmental management meetings.

5 Waste Management

In accordance with the Manual, the waste generated from construction activities was audited once per week to determine if wastes are being managed in accordance with the Waste Management Plan (WMP) prepared for the Project, contract-specific WMP, and any statutory and contractual requirements. All aspects of waste management including waste generation, storage, transportation and disposal were assessed during the audits.

5.1 Action and Limit Levels

The Action and Limit Levels of the construction waste are provided in **Table 5.1**.

Table 5.1: Action and Limit Levels for Construction Waste

Monitoring Stations	Action Level	Limit Level
Construction Area	When one valid documented complaint is received	Non-compliance of the WMP, contract-specific WMPs, any statutory and contractual requirements

5.2 Waste Management Status

Weekly monitoring on all works contracts were carried out by the ET to check and monitor the implementation of proper waste management practices during the construction phase.

Recommendations made included provision and maintenance of proper chemical waste storage area, as well as handling, segregation, and regular disposal of general refuse. The contractors have taken actions to implement the recommended measures. Waste management audits were carried out by ET according to the requirement of the Waste Management Plan, Updated EM&A Manual and the implementation schedule of the waste management mitigation measures in **Appendix A**.

Based on updated information provided by contractors, construction waste generated in the reporting period is summarised in **Table 5.2**. Dedicated areas for sorting of materials are established on site. Recyclable materials such as steel, reinforcement bar, structural steel, aluminum, copper, other metals and glass are sorted on-site and transported off-site for recycling. ET and IEC have carried out site audits regularly and reviewed the trip ticket system.

Table 5.2: Construction Waste Statistics

	C&D ⁽¹⁾ Material Stockpiled for Reuse or Recycle (m ³)	C&D Material Reused in the Project (m ³)	C&D Material Reused in other Projects (m ³)	C&D Material Transferred to Public Fill (m ³)	Chemical Waste (kg)	Chemical Waste (l)	General Refuse (tonne)
February 2022 ⁽²⁾⁽³⁾	32,167	31,937	582	3,219	0	0	2,403

Notes:

- (1) C&D refers to Construction and Demolition.
- (2) Metals, paper and/or plastics were recycled in the reporting period.
- (3) The data was based on the information provided by contractors up to the submission date of this Monthly EM&A Report, and might be updated in the forthcoming Monthly EM&A Report.

A complaint regarding general refuse was received in this reporting period. This complaint triggered the relevant Action Level, and the corresponding investigation was subsequently conducted in accordance with the Manual and the Complaint Management Plan of the Project. The summary of this complaint and analysis can be found in Section 7.9.1. On the other hand, there were no non-compliance of the WMP, contract-specific WMPs, statutory and contractual requirements that triggered Action and Limit Levels in this reporting period.

Along with the design and construction progress, further development on the treatment level/details and the re-use mode for marine sediment generated from 3RS Project has been conducted according to the EIA recommendation.

5.3 Marine Sediment Management

Marine sediment is managed according to the EIA Report, Updated EM&A Manual and Waste Management Plan of the Project. The sampling process, storage conditions of the excavated marine sediment, treatment process, final backfilling location as well as associated records were inspected and checked by ET and verified by IEC to ensure they were in compliance with the requirements as stipulated in the Waste Management Plan.

Sampling works for marine sediment generated from the reclaimed land area was on-going during the reporting period. The details of the marine sediment sampling, treatment and backfilling will be reported in the Annual EM&A Reports.

6 Chinese White Dolphin Monitoring

In accordance with the Manual, CWD monitoring by small vessel line-transect survey supplemented by land-based theodolite tracking survey and passive acoustic monitoring should be conducted during construction phase.

The small vessel line-transect survey should be conducted at a frequency of two full surveys per month, while land-based theodolite tracking survey should be conducted at a frequency of one day per month per station at Sha Chau (SC) and Lung Kwu Chau (LKC) during the construction phase as stipulated in the Manual.

6.1 Action and Limit Levels

The Action and Limit Levels for CWD monitoring were formulated by the action response approach using the running quarterly dolphin encounter rates STG and ANI derived from the baseline monitoring data, as presented in the CWD Baseline Monitoring Report. The derived values of Action and Limit Levels for CWD monitoring were summarised in **Table 6.1**.

Table 6.1: Derived Values of Action and Limit Levels for Chinese White Dolphin Monitoring

NEL, NWL, AW, WL and SWL as a Whole	
Action Level ⁽³⁾	Running quarterly ⁽¹⁾ STG < 1.86 & ANI < 9.35
Limit Level ⁽³⁾	Two consecutive running quarterly ⁽²⁾ (3-month) STG < 1.86 & ANI < 9.35

Notes: (referring to the baseline monitoring report)

- (1) Action Level – running quarterly encounter rates STG & ANI of this month will be calculated from the reporting period and the two preceding survey months.
- (2) Limit Level – two consecutive running quarters mean both the running quarterly encounter rates of the preceding month and the running quarterly encounter rates of this month.
- (3) Action Level and/or Limit Level will be triggered if both STG and ANI fall below the criteria.

6.2 CWD Monitoring Transects and Stations

6.2.1 Small Vessel Line-transect Survey

Small vessel line-transect surveys were conducted along the transects covering Northeast Lantau (NEL), Northwest Lantau (NWL), Airport West (AW), West Lantau (WL) and Southwest Lantau (SWL) areas as proposed in the Manual, which are consistent with the Agriculture, Fisheries and Conservation Department (AFCD) long-term monitoring programme (except the addition of AW). The AW transect has not been previously surveyed in the AFCD programme due to the restrictions of HKIA Approach Area, nevertheless, this transect was established during the EIA of the 3RS Project and refined in the Manual with the aim to collect project specific baseline information within the HKIA Approach Area to fill the data gap that was not covered by the AFCD programme. This also provided a larger sample size for estimating the density, abundance and patterns of movements in the broader study area of the project.

The planned vessel survey transect lines following the waypoints set for construction phase monitoring as proposed in the Manual are depicted in **Figure 6.1** with the waypoint coordinates of all transect lines given in **Table 6.2**, which are subject to on-site refinement based on the actual survey conditions and constraints.

Table 6.2: Coordinates of Transect Lines in NEL, NWL, AW, WL and SWL Survey Areas

Waypoint	Easting	Northing	Waypoint	Easting	Northing
NEL					
1S	813525	820900	6N	818568	824433
1N	813525	824657	7S	819532	821420
2S	814556	818449	7N	819532	824209
2N	814559	824768	8S	820451	822125
3S	815542	818807	8N	820451	823671
3N	815542	824882	9S	821504	822371
4S	816506	819480	9N	821504	823761
4N	816506	824859	10S	822513	823268
5S	817537	820220	10N	822513	824321
5N	817537	824613	11S	823477	823402
6S	818568	820735	11N	823477	824613
NWL					
1S	804671	814577	5S	808504	821735
1N	804671	831404	5N	808504	828602
2Sb	805475	815457	6S	809490	822075
2Nb	805476	818571	6N	809490	825352
2Sa	805476	820770	7S	810499	822323
2Na	805476	830562	7N	810499	824613
3S	806464	821033	8S	811508	821839
3N	806464	829598	8N	811508	824254
4S	807518	821395	9S	812516	821356
4N	807518	829230	9N	812516	824254
AW					
1W	804733	818205	2W	805045	816912
1E	806708	818017	2E	805960	816633
WL					
1W	800600	805450	7W	800400	811450
1E	801760	805450	7E	802400	811450
2W	800300	806450	8W	800800	812450
2E	801750	806450	8E	802900	812450
3W	799600	807450	9W	801500	813550
3E	801500	807450	9E	803120	813550
4W	799400	808450	10W	801880	814500
4E	801430	808450	10E	803700	814500
5W	799500	809450	11W	802860	815500
5E	801300	809450	12S/11E	803750	815500
6W	799800	810450	12N	803750	818500
6E	801400	810450			
SWL					
1S	802494	803961	6S	807467	801137
1N	802494	806174	6N	807467	808458
2S	803489	803280	7S	808553	800329
2N	803489	806720	7N	808553	807377
3S	804484	802509	8S	809547	800338
3N	804484	807048	8N	809547	807396
4S	805478	802105	9S	810542	800423
4N	805478	807556	9N	810542	807462
5S	806473	801250	10S	811446	801335

Waypoint	Easting	Northing	Waypoint	Easting	Northing
5N	806473	808458	10N	811446	809436

6.2.2 Land-based Theodolite Tracking Survey

Land-based theodolite tracking survey stations were set up at two locations, one facing east/south/west on the southern slopes of Sha Chau (SC), and the other facing north/northeast/northwest at Lung Kwu Chau (LKC). The stations (D and E) are depicted in **Figure 6.2** and shown in **Table 6.3** with position coordinates, height of station and approximate distance of consistent theodolite tracking capabilities for CWD.

Table 6.3: Land-based Theodolite Survey Station Details

Stations	Location	Geographical Coordinates	Station Height (m)	Approximate Tracking Distance (km)
D	Sha Chau (SC)	22° 20' 43.5" N 113° 53' 24.66" E	45.66	2
E	Lung Kwu Chau (LKC)	22° 22' 44.83" N 113° 53' 0.2" E	70.40	3

6.3 CWD Monitoring Methodology

6.3.1 Small Vessel Line-transect Survey

Small vessel line-transect surveys provided data for density and abundance estimation and other assessments using distance-sampling methodologies, specifically, line-transect methods.

The surveys involved small vessel line-transect data collection and have been designed to be similar to, and consistent with, previous surveys for the AFCD for their long-term monitoring of small cetaceans in Hong Kong. The survey was designed to provide systematic, quantitative measurements of density, abundance and habitat use.

As mentioned in **Section 6.2.1**, the transects covered NEL, NWL, AW, WL and SWL areas as proposed in the Manual, which are consistent with the AFCD long-term monitoring programme (except AW). There are two types of transect lines:

- Primary transect lines: the parallel and zigzag transect lines as shown in **Figure 6.1**; and
- Secondary transect lines: transect lines connecting between the primary transect lines and going around islands.

All data collected on both primary and secondary transect lines were used for analysis of sighting distribution, group size, activities including association with fishing boat, and mother-calf pairs. Only on-effort data collected under favourable conditions of Beaufort 0-3 and visibility of approximately 1200 m or beyond were used for analysis of the CWD encounter rates.

A 15-20m vessel with a flying bridge observation platform about 4 to 5m above water level and unobstructed forward view, and a team of three to four observers were deployed to undertake the surveys. Two observers were on search effort at all times when following the transect lines with a constant speed of 7 to 8 knots (i.e. 13 to 15 km per hour), one using 7X handheld binoculars and the other using unaided eyes and recording data.

During on-effort survey periods, the survey team recorded effort data including time, position (waypoints), weather conditions (Beaufort sea state and visibility) and distance travelled in each series with assistance of a handheld GPS device. The GPS device also continuously and automatically logged data including time, position (latitude and longitude) and vessel speed throughout the entire survey.

When CWDs were seen, the survey team was taken off-effort, the dolphins were approached and photographed for photo-ID information (using a Canon 7D [or similar] camera and long 300 mm+ telephoto lens), then followed until they were lost from view. At that point, the boat returned (off effort) to the survey line at the closest point after obtaining photo records of the dolphin group and began to survey on effort again.

Focal follows of dolphins would be used for providing supplementary information only where practicable (i.e. when individual dolphins or small stable groups of dolphins with at least one member that could be readily identifiable with unaided eyes during observations and weather conditions are favourable). These would involve the boat following (at an appropriate distance to minimise disturbance) an identifiable individual dolphin for an extended period of time, and collecting detailed data on its location, behaviour, response to vessels, and associates.

6.3.2 Photo Identification

CWDs can be identified by their unique features like presence of scratches, nick marks, cuts, wounds, deformities of their dorsal fin and distinguished colouration and spotting patterns.

When CWDs were observed, the survey team was taken off-effort, the dolphins were approached and photographed for photo-ID information (using a Canon 7D [or similar] camera and long 300 mm+ telephoto lens). The survey team attempted to photograph both sides of every single dolphin in the group as the colouration and spotting pattern on both sides may not be identical. The photos were taken at the highest available resolution and stored on Compact Flash memory cards for transferring into a computer.

All photos taken were initially examined to sort out those containing potentially identifiable individuals. These sorted-out images would then be examined in detail and compared to the CWD photo-identification catalogue established for 3RS Project during the baseline monitoring stage.

6.3.3 Land-based Theodolite Tracking Survey

Land-based theodolite tracking survey obtains fine-scale information on the time of day and movement patterns of the CWDs. A digital theodolite (Sokkia/Sokkisha Model DT5 or similar equipment) with 30-power magnification and 5-s precision was used to obtain the vertical and horizontal angle of each dolphin and vessel position. Angles were converted to geographic coordinates (latitude and longitude) and data were recorded using *Pythagoras* software, Version 1.2. This method delivers precise positions of multiple spatially distant targets in a short period of time. The technique is fully non-invasive, and allows for time and cost-effective descriptions of dolphin habitat use patterns at all times of daylight.

Three surveyors (one theodolite operator, one computer operator, and one observer) were involved in each survey. Observers searched for dolphins using unaided eyes and handheld binoculars (7X50). Theodolite tracking sessions were initiated whenever an individual CWD or group of CWDs was located. Where possible, a distinguishable individual was selected, based on colouration, within the group. The focal individual was then continuously tracked via the theodolite, with a position recorded each time the dolphin surfaced. In case an individual could not be positively distinguished from other members, the group was tracked by recording positions based on a central point within the group whenever the CWD surfaced. Tracking continued until animals were lost from view; moved beyond the range of reliable visibility (>1-3km, depending on station height); or environmental conditions obstructed visibility (e.g., intense haze, Beaufort sea state >4, or sunset), at which time the research effort was terminated. In addition to the tracking of CWD, all vessels that moved within 2-3km of the station were tracked, with effort made to obtain at least two positions for each vessel.

Theodolite tracking included focal follows of CWD groups and vessels. Priority was given to tracking individual or groups of CWD. The survey team also attempted to track all vessels moving within 1 km of the focal CWD.

6.4 Monitoring Results and Observations

6.4.1 Small Vessel Line-transect Survey

Survey Effort

Within this reporting period, two complete sets of small vessel line-transect surveys were conducted on the 7, 8, 9, 10, 14 and 15 February, 2 March and 4 March 2022 covering all transects in NEL, NWL, AW, WL and SWL survey areas for twice. There were two survey days for this period (in SWL survey area) rescheduled to early March due to unavailability of vessel operators or suitable vessel during the rising impact of COVID-19 pandemic in the second half of February.


A total of around 444.61km of survey effort was collected from these surveys and 413.42 km of the survey effort was being conducted under favourable weather condition (i.e. Beaufort Sea State 3 or below with favourable visibility). Details of the survey effort are given in **Appendix C**.

Sighting Distribution

In the current reporting period, seven sightings with 22 dolphins were sighted. All these sightings were on-effort records under favourable weather condition (i.e. Beaufort Sea State 3 or below with favourable visibility). Details of cetacean sightings are presented in **Appendix C**.

Distribution of all CWD sightings recorded in the current reporting period is illustrated in **Figure 6.3**. In WL, CWD groups were recorded along waters off north of Yi O to Peaked Hill. In SWL, there was a CWD group recorded at waters near Fan Lau. In NWL, the CWD groups were spotted at waters near Lung Kwu Chau and west of airport area. There was no CWD sighting recorded in NEL survey area during the reporting period.

Figure 6.3: Sightings Distribution of Chinese White Dolphins

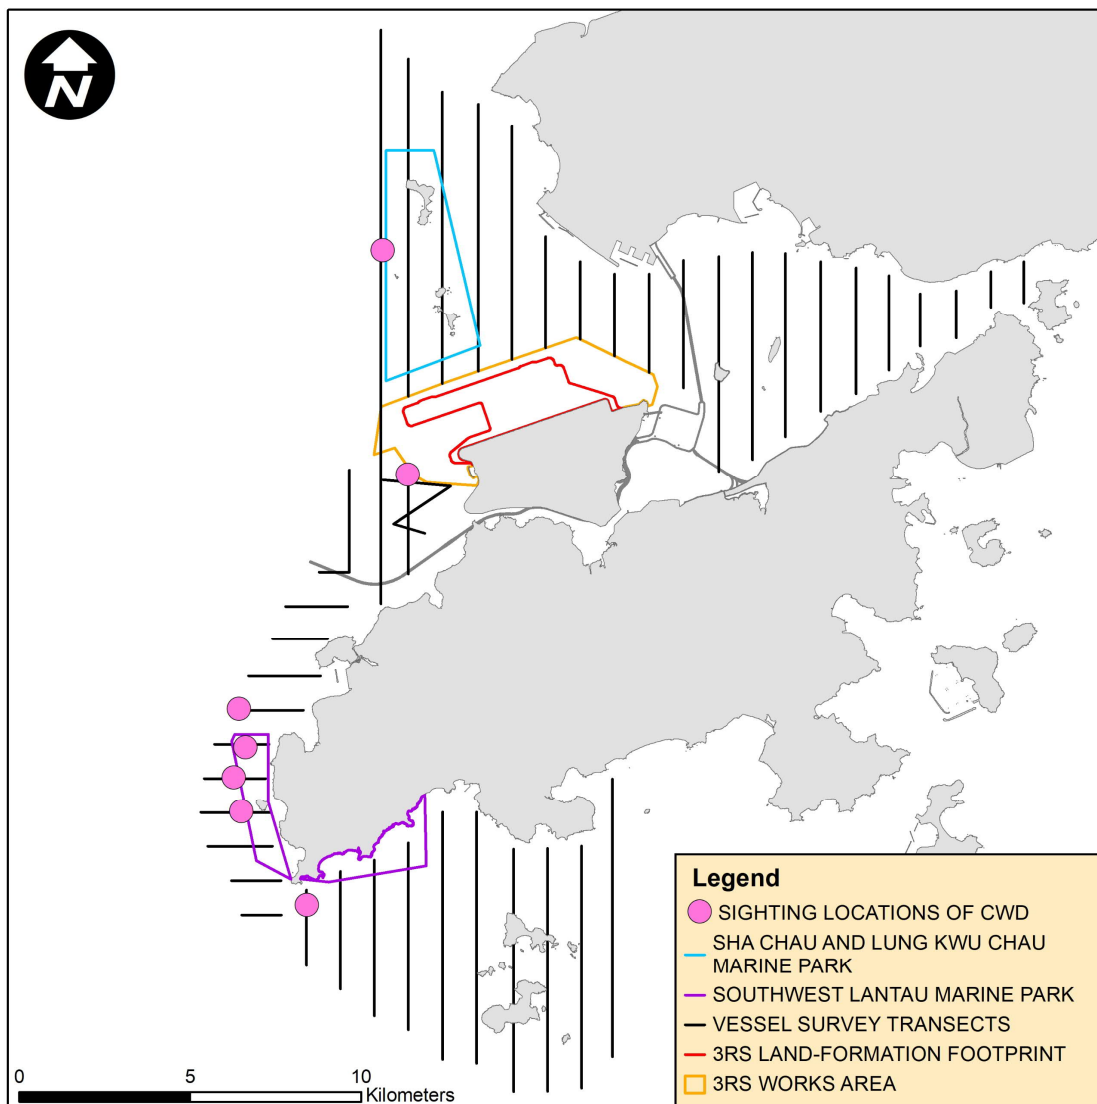

Remarks: (1) Please note that there are seven pink circles on the map indicating the sighting locations of CWDs. Some of them were very close to each other and therefore may appear overlapped on this distribution map. (2) Marine park excludes land area and the landward boundary generally follows the high water mark along the coastline.

Encounter Rate

Two types of dolphin encounter rates were calculated based on the vessel survey data. They included the number of dolphin sightings per 100 km survey effort (STG) and total number of dolphins per 100 km survey effort (ANI) in the whole survey area (i.e. NEL, NWL, AW, WL and SWL). In the calculation of dolphin encounter rates, only survey data collected under favourable weather condition (i.e. Beaufort Sea State 3 or below with favourable visibility) were used. The formulae used for calculation of the encounter rates are shown below:

Encounter Rate by Number of Dolphin Sightings (STG)

$$STG = \frac{\text{Total No. of On-effort Sightings}}{\text{Total Amount of Survey Effort (km)}} \times 100$$

Encounter Rate by Number of Dolphins (ANI)

$$ANI = \frac{\text{Total No. of Dolphins from On-effort Sightings}}{\text{Total Amount of Survey Effort (km)}} \times 100$$

(Notes: Only data collected under Beaufort 3 or below condition were used)

In this reporting period, a total of around 413.42 km of survey effort were conducted under Beaufort Sea State 3 or below with favourable visibility, whilst a total number of seven on-effort sightings with 22 dolphins were sighted under such condition. Calculation of the encounter rates for the month are shown in **Appendix C**.

For the running quarter of the reporting period (i.e., from December 2021 to February 2022, including the two survey days rescheduled to early March 2022), a total of around 1206.56 km of survey effort were conducted under Beaufort Sea State 3 or below with favourable visibility, whilst a total number of 35 on-effort sightings and a total number of 123 dolphins from on-effort sightings were obtained under such condition. Calculation of the running quarterly encounter rates are shown in **Appendix C**.

The STG and ANI of CWD in the whole survey area (i.e. NEL, NWL, AW, WL and SWL) during the reporting period and during the running quarter are presented in **Table 6.4** below and compared with the Action Level. The running quarterly encounter rates STG and ANI remain above the Action Level, thus the Action Level is not triggered.

Table 6.4: Comparison of CWD Encounter Rates of the Whole Survey Area with Action Levels

	Encounter Rate (STG)	Encounter Rate (ANI)
February 2022	1.69	5.32
Running Quarter from December 2021 to February 2022 ⁽¹⁾	2.90	10.19
Action Level	Running quarterly ⁽¹⁾ STG < 1.86 & ANI < 9.35	

Note: (1) Running quarterly encounter rates STG & ANI were calculated from data collected in the reporting period and the two preceding survey months, containing six sets of transect surveys for all monitoring areas. Action Level will be triggered if both STG and ANI fall below the criteria.

Group Size

In the current reporting period, seven groups of 22 dolphins in total were sighted, and the average group size of CWDs was 3.1 dolphins per group. Numbers of CWD sightings with small group size (i.e. 1-2 dolphins) and medium group size (i.e. 3-9 dolphins) were similar. No CWD sighting with large group size (i.e. 10 or more dolphins) was recorded this reporting period.

Activities and Association with Fishing Boats

Only one CWD sighting was recorded engaging in feeding activities in the current reporting period with no association with operating fishing boat.

Mother-calf Pair

In this reporting period, there was one CWD sighting recorded with mother-and-unspotted juvenile pair in WL survey area.

6.4.2 Photo Identification

In the current reporting period, a total number of nine different CWD individuals were identified for totally nine times. A summary of photo identification works is presented in **Table 6.5**. Representative photos of these individuals are given in **Appendix C**.

Table 6.5: Summary of Photo Identification

Individual ID	Date of Sighting (dd-mm-yy)	Sighting Group No.	Area	Individual ID	Date of Sighting (dd-mm-yy)	Sighting Group No.	Area
NLMM013	15-Feb-22	1	NWL	WLMM028	10-Feb-22	1	WL
NLMM028	15-Feb-22	1	NWL	WLMM109	10-Feb-22	1	WL
SLMM007	10-Feb-22	1	WL	WLMM114	10-Feb-22	1	WL
SLMM073	10-Feb-22	1	WL	WLMM152	10-Feb-22	1	WL
WLMM019	15-Feb-22	1	NWL				

6.4.3 Land-based Theodolite Tracking Survey

Survey Effort

Land-based theodolite tracking surveys were conducted at LKC on 11 February 2022 and at SC on 16 February 2022, with a total of two days of land-based theodolite tracking survey effort accomplished in this reporting period. An individual of CWD was tracked off LKC station during the reporting period. Information of survey effort and CWD groups are presented in **Table 6.6**. Details of the survey effort are presented in **Appendix C**. The first sighting location of CWD group tracked at LKC station during land-based theodolite tracking survey in February 2022 was depicted in **Figure 6.4**.

Table 6.6: Summary of Survey Effort and CWD Group of Land-based Theodolite Tracking

Land-based Station	No. of Survey Sessions	Survey Effort (hh:mm)	No. of CWD Groups Sighted	CWD Group Sighting per Survey Hour
Lung Kwu Chau	1	6:00	1	0.167
Sha Chau	1	6:00	0	0
TOTAL	2	12:00	1	0.083

Figure 6.4: Plots of First Sightings of All CWD Groups obtained from Land-based Stations



6.5 Progress Update on Passive Acoustic Monitoring

Underwater acoustic monitoring using Passive Acoustic Monitoring (PAM) should be undertaken during land formation related construction works. Both C-POD and F-POD are considered as effective PAM devices in detecting CWD occurrence, and F-POD was the main PAM device deployed where feasible. During this reporting period, the F-POD was remained underwater and position at south of Sha Chau Island inside the SCLKCMP (**Figure 6.5**). It was last deployed on 10 January 2022 and the next retrieval is scheduled in early March. Acoustic data would be reviewed to give an indication of CWDs occurrence patterns and anthropogenic noise information. Analysis would involve use of proprietary software for objective automated data analyses and experienced analysts to perform visual validation for assessment of dolphin detection. As the period of data collection and analysis takes about four months, PAM results could not be reported in monthly intervals but report for supplementing the annual CWD monitoring analysis.

6.6 Site Audit for CWD-related Mitigation Measures

During the reporting period, 1 dolphin observation station and teams of at least two dolphin observers were deployed by the contractors for continuous monitoring of the DEZ for DCM related works in accordance with the DEZ Plan. Trainings for the proposed dolphin observers on the implementation of MMWP and DEZ monitoring were provided by the ET prior to the aforementioned works, with a cumulative total of 704 individuals being trained and the training records kept by the ET. From the contractors' DEZ monitoring records, no dolphin or other marine mammals were observed within or around the DEZs in this reporting month. These contractors' records were also audited by the ET during site inspection.

Audits of acoustic decoupling measures for construction vessels were carried out during weekly site inspection and the observations are summarised in **Section 7.1**. Audits of SkyPier high speed ferries route diversion and speed control and construction vessel management are presented in **Section 7.4** and **Section 7.5** respectively.

6.7 Timing of reporting CWD Monitoring Results

Detailed analysis of CWD monitoring results collected by small vessel line-transect survey will be provided in future quarterly reports. Detailed analysis of CWD monitoring results collected by land-based theodolite tracking survey and PAM will be provided in future annual reports after a larger sample size of data has been collected.

6.8 Summary of CWD Monitoring

Monitoring of CWD was conducted with two complete sets of small vessel line-transect surveys and two days of land-based theodolite tracking survey effort. The running quarterly encounter rates STG and ANI in the reporting period did not trigger the Action Level for CWD monitoring.

7 Environmental Site Inspection and Audit

7.1 Environmental Site Inspection

Due to the COVID-19 pandemic, virtual and physical site inspections of the construction works to audit the implementation of proper environmental pollution control and mitigation measures for the Project were conducted by ET and IEC on a weekly and bi-weekly basis, respectively. The weekly site inspection schedule of the construction works is provided in **Appendix B**. Besides, physically ad-hoc site inspections were also conducted by ET and IEC if environmental problems were identified, or subsequent to receipt of an environmental complaint, or as part of the investigation work. These site inspections provided a direct means to reinforce the specified environmental protection requirements and pollution control measures in construction sites.

During site inspections, environmental situation, status of implementation of pollution control and mitigation measures were observed. Environmental documents and site records, including waste disposal record, maintenance record of environmental equipment, and relevant environmental permit and licences, were also checked on site. Observations were recorded in the site inspection checklist and passed to the contractor together with the recommended mitigation measures where necessary in order to advise contractors on environmental improvement, awareness and on-site enhancement measures. The observations were made with reference to the following information during the site inspections:

- The EIA and EM&A requirements;
- Relevant environmental protection laws, guidelines, and practice notes;
- The EP conditions and other submissions under the EP;
- Monitoring results of EM&A programme;
- Works progress and programme;
- Proposal of individual works;
- Contract specifications on environmental protection; and
- Previous site inspection results.

Good site practices were observed in site inspections during the reporting period. Advice was given when necessary to ensure the construction workforce were familiar with relevant procedures, and to maintain good environmental performance on site. Regular toolbox talks on environmental issues were organised for the construction workforce by the contractors to ensure understanding and proper implementation of environmental protection and pollution control mitigation measures.

A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix A**.

7.2 Landscape and Visual Mitigation Measures

Implementation of applicable landscape and visual mitigation measures (reference to the environmental protection measures CM1 – CM10 in **Appendix A**) was monitored in accordance with the Manual. All measures undertaken by both the contractor and the landscape contractor during the construction phase and first year of the operation phase shall be audited by a landscape architect, as a member of the ET, on a regular basis to ensure compliance with the intended aims of the measures. Site inspections shall be undertaken at least once every two months during the operation phase.

The implementation status of the environmental protection measures is summarized below in **Table 7.1**. Examples of landscape and visual mitigation measures are shown in **Table 7.2**. The

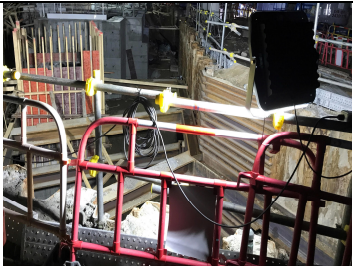
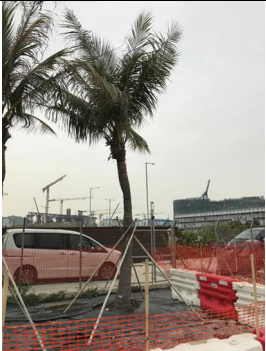
monitoring programme for detailed design, construction, establishment works and long term management (10 years) stages is presented in **Table 7.3**. Event and Action Plan for Landscape and Visual impacts is stated in **Table 7.4**.

Table 7.1: Landscape and Visual – Construction Phase Audit Summary

Landscape and Visual Mitigation Measures during Construction	Implementation Status	Relevant Contract(s) in the Reporting Period
CM1- The construction area and contractor's temporary works areas shall be minimised to avoid impacts on adjacent landscape.	The implementation of mitigation measures was checked by ET during weekly site inspection and reported by the Contractors during the monthly Environmental Management Meetings. Implementation of the measures CM5, CM6 and CM7 by Contractors was observed.	All works contracts
CM2 – Reduction of construction period to practical minimum		
CM3 – Phasing of the construction stage to reduce visual impacts during the construction phase.		
CM4 – Construction traffic (land and sea) including construction plants, construction vessels and barges shall be kept to a practical minimum.		
CM5 – Erection of decorative mesh screens or construction hoardings around works areas in visually unobtrusive colours.		
CM6 – Avoidance of excessive height and bulk of site buildings and structures		
CM7 – Control of night-time lighting by hooding all lights and through minimisation of night working periods		
CM8 – All existing trees shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas	Tree Protection Specifications were provided in the relevant Contract Specifications respectively for implementation by the Contractors under the Project. The Contractors' performance on the implementation of the tree maintenance and protection measures were observed and checked by the ET weekly during construction period.	3302, 3503, 3508, 3602, 3801 3802 (To be implemented)

Landscape and Visual Mitigation Measures during Construction	Implementation Status	Relevant Contract(s) in the Reporting Period
CM9 – Trees unavoidably affected by the works shall be transplanted where practical. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	Tree Transplanting Specifications were provided in the relevant Contract Specifications respectively for implementation by the Contractors under the Project where trees would unavoidably be affected by the construction works. The Contractors were required to submit Method Statements for tree transplanting prior to the transplanting works. Tree inspections were conducted by ET to check the tree transplanting works implemented by the Contractors on site. The Contractors' performance on the implementation of trees maintenance and protection measures on transplanted trees were observed and checked by the ET bi-monthly during the 12-month establishment period after the completion of each batch of transplanting works. Long term management of the transplanted trees was currently monitored by ET annually.	3503, 3508, 3801 3802 (To be implemented)
CM10 – Land formation works shall be followed with advanced hydroseeding around taxiways and runways as soon as practical	To be implemented around taxiways and runways as soon as practicable.	3303

Table 7.2: Examples of Landscape and Visual Mitigation Measures in the Reporting Period

		
Erection of site hoardings around works area in unobtrusive colours (CM5)	Avoidance of excessive height and bulk of site buildings (CM6)	Control of night-time lighting using light hooding and minimisation of night working period (CM7)
		
General view of tree protection zone for retained tree (CM8)	General view of a transplanted tree (CM9)	General view of advanced hydroseeding around taxiways and runways (CM10)

In accordance with the Updated EM&A Manual, all existing trees shall be protected carefully during construction. Trees unavoidably affected by the works shall be transplanted where practical. In this reporting period, the cumulative total number of retained and transplanted trees under the Project remained unchanged (i.e. 52 and 26 respectively) comparing to the previous reporting period. Details of the retained trees, transplanted trees and to-be-transplanted trees under the Project are summarized in **Table 7.5**.

Details of the retained trees are to be discussed in the Quarterly EM&A reports.

Table 7.3: Monitoring Programme for Landscape and Visual

Stage	Monitoring Task	Monitoring Report	Form of Approval	Frequency
Detailed Design	Checking of design works against the recommendations of the landscape and visual impact assessments within the EIA shall be undertaken during detailed design and tender stage, to ensure that they fulfil the intention of the mitigation measures. Any changes to the design, including design changes on site shall also be checked.	Report by AAHK / PM confirming that the design conforms to requirements of EP.	Approved by Client	At the end of the Detailed Design Phase
Construction	Checking of the contractor's operations during the construction period.	Report on Contractor's compliance, by ET	Counter signature of report by IEC	Weekly
Establishment Works	Checking of the planting works during the twelve-month Establishment Period after completion of each batch of transplanting works.	Report on Contractor's compliance, by ET	Counter signature of report by IEC	Every two months
Long Term Management (10 year)	Monitoring of the long-term management of the planting works in the period up to 10 years after completion of each batch of transplanting works.	Report on Compliance by ET or Maintenance Agency as appropriate	Counter signature of report by Management Agency	Annually

Table 7.4: Event and Action Plan for Landscape and Visual

Event Action Level	Action			
	ET	IEC	AAHK / PM	Contractor
Design Check	Check final design conforms to the requirements of EP and prepare report.	Check report. Recommend remedial design if necessary.	Undertake remedial design if necessary.	
Non-conformity on one occasion	Identify source.	Check report.	Notify Contractor.	Amend working methods to prevent

Event Action Level	Action			
	Inform IEC and AAHK / PM. Discuss remedial actions with IEC, AAHK / PM and Contractor. Monitor remedial actions until rectification has been completed.	Check Contractor's working method. Discuss with ET and Contractor on possible remedial measures. Advise AAHK / PM on effectiveness of proposed remedial measures. Check implementation of remedial measures.	Ensure remedial measures are properly implemented.	recurrence of non-conformity. Rectify damage and undertake additional action necessary.
Repeated Non-conformity	Identify source. Inform IEC and AAHK / PM. Increase monitoring frequency. Discuss remedial actions with IEC, AAHK / PM and Contractor. Monitor remedial actions until rectification has been completed. If non-conformity stops, cease additional monitoring.	Check monitoring report. Check Contractor's working method. Discuss with ET and Contractor on possible remedial measures. Advise AAHK / PM on effectiveness of proposed remedial measures. Supervise implementation of remedial measures.	Notify Contractor. Ensure remedial measures area properly implemented.	Amend working methods to prevent recurrence of non-conformity. Rectify damage and undertake additional action necessary.

Table 7.5: Summary of the Number of Retained, Transplanted and To-be-transplanted Trees in the Reporting Period

Existing				
Contract	Retain (nos.)	Transplanted (nos.)		To-be-transplanted (nos.)
		Establishment Period	Maintenance Period	
3302	9	0	0	0
3503	0	0	9	0
3508 ⁽¹⁾	24	12	0	0
3602	2	0	0	0
3801	17	0	5 ⁽²⁾	0
Sub-total	52	12	14	0
Provisional				
Contract	Retain (nos.)	Transplanted (nos.)		To-be-transplanted (nos.)
3508 ⁽¹⁾	51	0		10
Sub-total	51	0		10
Grand Total	103	26		10

Notes:

- (1) As some of the site areas have been handed over to Contract 3508, Contractor of Contract 3508 is currently managing the trees that are located within their site area. Existing trees to be managed by Contract 3508 is subject to change after initial tree surveys for each batch of site areas have been conducted by the Contractor.
- (2) Three transplanted trees (CT1194, CT1794 and CT1795) were subsequently felled after transplantation. Please refer to **Table 7.6** for details.

Summary of the updated transplanted trees and photos are presented in **Table 7.6** and **Table 7.7** respectively.


Table 7.6: Summary of the Transplanted Trees Updated in the Reporting Period

Tree ID	Transplant Date	Management Stage	Management Agency	Remarks
CT276	3 May 2018	<u>Establishment period</u> 4 May 2018 – May 2019	Contract 3801	Next inspection will be conducted in February 2023. Photos of the last inspection in February 2022 were shown in Table 7.7 .
		<u>Long Term Management period</u> Jun 2019 – May 2028	Southern Landside Petrol Filling Station	
CT1253	4 May 2018	<u>Establishment period</u> 5 May 2018 – May 2019	Contract 3801	
		<u>Long Term Management period</u> Jun 2019 – May 2028	Southern Landside Petrol Filling Station	
T835	22 Jan 2020	<u>Establishment period</u> 23 Jan 2020 – Jan 2021	Contract 3503	Next inspection will be conducted in February 2023. Photos of the last inspection in February 2022 were shown in Table 7.7 .
		<u>Long Term Management period</u> Feb 2021 – Jan 2030		
T836	13 Dec 2019	<u>Establishment period</u> 14 Dec 2020 – Jan 2021	Contract 3503	
		<u>Long Term Management period</u> Feb 2021 – Jan 2030		
T838	22 Jan 2020	<u>Establishment period</u> 23 Jan 2020 – Jan 2021	Contract 3503	
		<u>Long Term Management period</u> Feb 2021 – Jan 2030		
T812	21 Dec 2020	<u>Establishment period</u> 22 Dec 2020 – Dec 2021	Contract 3503	Next inspection will be conducted in December 2022. Photos of the last inspection in December 2021 can be referred to Table 7.7 of the Construction Phase Monthly EM&A Report No.72.
		<u>Long Term Management period</u> Jan 2022 – Dec 2031		
T814	20 Dec 2020	<u>Establishment period</u> 21 Dec 2020 – Dec 2021	Contract 3503	
		<u>Long Term Management period</u> Jan 2022 – Dec 2031		
T815	15 Dec 2020	<u>Establishment period</u> 16 Dec 2020 – Dec 2021	Contract 3503	
		<u>Long Term Management period</u> Jan 2022 – Dec 2031		
T829	18 Dec 2020	<u>Establishment period</u> 19 Dec 2020 – Dec 2021	Contract 3503	
		<u>Long Term Management period</u> Jan 2022 – Dec 2031		

Tree ID	Transplant Date	Management Stage	Management Agency	Remarks
T830	14 Dec 2020	<u>Establishment period</u> 15 Dec 2020 – Dec 2021 <u>Long Term Management period</u> Jan 2022 – Dec 2031	Contract 3503	
T831	19 Dec 2020	<u>Establishment period</u> 20 Dec 2020 – Dec 2021 <u>Long Term Management period</u> Jan 2022 – Dec 2031	Contract 3503	
T1493	6 Jul 2021	<u>Establishment period</u> 7 Jul 2021 – Jul 2022	Contract 3508	Next inspection will be conducted in March 2022. Photos of the last inspection in January 2022 can be referred to Table 7.7 of the Construction Phase Monthly EM&A Report No.73.
T1494	6 Jul 2021	<u>Establishment period</u> 7 Jul 2021 – Jul 2022	Contract 3508	
T1495	10 Jul 2021	<u>Establishment period</u> 11 Jul 2021 – Jul 2022	Contract 3508	
T1496	5 Jul 2021	<u>Establishment period</u> 6 Jul 2021 – Jul 2022	Contract 3508	
T1497	5 Jul 2021	<u>Establishment period</u> 6 Jul 2021 – Jul 2022	Contract 3508	
T1498	29 Jun 2021	<u>Establishment period</u> 30 Jun 2021 – Jul 2022	Contract 3508	
T1499	29 Jun 2021	<u>Establishment period</u> 30 Jun 2021 – Jul 2022	Contract 3508	
T1500	30 Jun 2021	<u>Establishment period</u> 1 Jul 2021 – Jul 2022	Contract 3508	
T1501	30 Jun 2021	<u>Establishment period</u> 1 Jul 2021 – Jul 2022	Contract 3508	
T1502	5 Jul 2021	<u>Establishment period</u> 6 Jul 2021 – Jul 2022	Contract 3508	
T1503	6 Jul 2021	<u>Establishment period</u> 7 Jul 2021 – Jul 2022	Contract 3508	
T1504	24 Jun 2021	<u>Establishment period</u> 25 Jun 2021 – Jul 2022	Contract 3508	
CT1194	4 May 2018	<u>Establishment period</u> 5 May 2018 – May 2019	Contract 3801	NA
		<u>Long Term Management period</u> Jun 2019 – May 2028	Southern Landside Petrol Filling Station	Uprooted and collapsed due to Typhoon Higos on 18 August 2020. Tree removal was conducted as recommended by tree specialist of the contractor of Southern Landside Petrol Filling Station.
CT1794	3 May 2018	<u>Establishment period</u> 4 May 2018 – May 2019	Contract 3801	NA
		<u>Long Term Management period</u>	AsiaWorld-Expo	The tree within the land parcel was acquired by the government for construction of emergency hospital

Tree ID	Transplant Date	Management Stage	Management Agency	Remarks
		Jun 2019 – May 2028		to handle COVID19 pandemic at AsiaWorld-Expo. The tree was felled in late 2020.
CT1795	3 May 2018	<u>Establishment period</u> 4 May 2018 – May 2019	Contract 3801	NA
		<u>Long Term Management period</u> Jun 2019 – May 2028	AsiaWorld-Expo	The tree within the land parcel was acquired by the government for construction of emergency hospital to handle COVID19 pandemic at AsiaWorld-Expo. The tree was felled in late 2020.

Table 7.7: Photos of the Existing Transplanted Trees Inspected in this Reporting Month

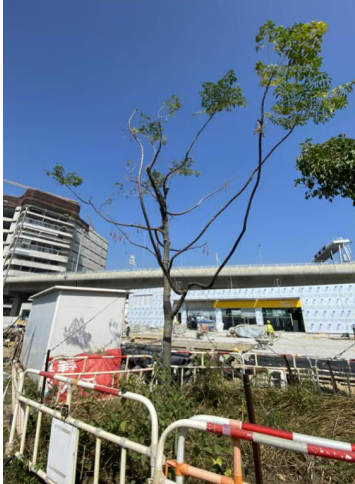Under 10-year Long-term Management:		
		
CT276	CT1253	T835
		
T836	T838	

7.3 Land Contamination Assessment

The Supplementary CAP was submitted to EPD pursuant to EP Condition 2.20. The CARs for Golf Course and T2 Emergency Power Supply Systems (EPSS) were submitted to EPD in accordance with EP Condition 1.9 and the Supplementary CAP in which no land contamination issues were identified. EPD has issued no further comment for aforesaid CARs. No leakage was

found after the removal of underground fuel pipelines of T2 EPSS and all required additional photos have been submitted to EPD.

According to the approved supplementary CAP, there are 3 remaining locations where site re-appraisal / additional site investigation are proposed. Based on the latest construction information, there is no development programme for these locations at this stage. As such, the status of site re-appraisal/ additional site investigation shall be further updated upon latest development programme is available.

7.4 Audit of SkyPier High Speed Ferries

The Marine Travel Routes and Management Plan for High Speed Ferries of SkyPier (the SkyPier Plan) was submitted to the Advisory Council on the Environment for comment and subsequently submitted to and approved by EPD in November 2015 under EP Condition 2.10. The approved SkyPier Plan is available on the dedicated website of the Project. In the SkyPier Plan, AAHK has committed to implement the mitigation measure of requiring HSFs of SkyPier travelling between HKIA and Zhuhai / Macau to start diverting the route with associated speed control across the area, i.e. Speed Control Zone (SCZ), with high CWD abundance. The route diversion and speed restriction at the SCZ have been implemented since 28 December 2015.

Due to the COVID-19 pandemic, all SkyPier HSF services to/from Zhuhai and Macau have been suspended from 25 March 2020 until further notice. No ferry movement between HKIA SkyPier and Zhuhai and Macau was recorded in February 2022. Key audit findings for the SkyPier HSFs travelling to/from Zhuhai and Macau against the requirements of the SkyPier Plan during the reporting period are summarised in **Table 7.8**.

The daily movement of all SkyPier HSFs, including those not using the diverted route, in this reporting period (i.e., 3 to 4 daily movements) were within the maximum daily cap of 125 daily movements. Status of compliance with the annual daily average of 99 movements will be further reviewed in the Annual EM&A Report.

As updated by CLP Power, the construction works of the Hong Kong Offshore LNG Terminal Project may affect the route diversion operation of the SkyPier HSFs from Q1 to Q2 2022. The captains were informed on the issue and ET will continue to closely monitor the implementation of the SkyPier Plan in the period.

Table 7.8: Summary of Key Audit Findings against the SkyPier Plan

Requirements in the SkyPier Plan	1 to 28 February 2022
Total number of ferry movements recorded and audited for HSF to/from Zhuhai and Macau	0
Use diverted route and enter / leave SCZ through Gate Access Points	0 deviation
Daily Cap for all SkyPier HSFs including those not using diverted route	3 to 4 daily movement (within the maximum daily cap - 125 daily movements)

7.5 Audit of Construction and Associated Vessels

The updated Marine Travel Routes and Management Plan for Construction and Associated Vessel (MTRMP-CAV) was submitted and approved in May 2020 by EPD under EP Condition 2.9. The approved Plan is available on the dedicated website of the Project.

ET carried out the following actions during the reporting period:

- Based on the updated record, 4 skippers were trained by contractors' Environmental Officers in the previous period. In total, 1849 skippers were trained from August 2016 to February 2022.
- The MSS automatically recorded deviation cases such as speeding, entering no entry zone and not travelling through the designated gate. ET conducted checking to ensure the MSS records deviation cases accurately.
- Deviations such as speeding in the works area, entered no entry zone, and entering from non-designated gates were identified. All the concerned contractors were reminded to comply with the requirements of the MTRMP-CAV during the bi-weekly Construction Traffic Control Centre (CTCC) audit.
- Three-month rolling programmes (one month record and three months forecast) for construction vessel activities were received from the contractors in order to help maintain the number of construction and associated vessels on site to a practicable minimal level.

7.6 Implementation of Dolphin Exclusion Zone

The DEZ Plan was submitted in accordance with EP Condition 3.1 (v) requirement and Section 10.3 of the Manual, and approved in April 2016 by EPD. The 24-hour DEZs with a 250m radius for marine works were established and implemented by the contractors for DCM and seawall construction according to their Method Statement for DEZ Monitoring that followed the specifications and requirements of the DEZ Plan.

During the reporting period, ET was notified that no dolphin sightings were recorded within the DEZ by the contractors. The ET checked the dolphin sighting record and relevant records by the contractors to audit the implementation of DEZ.

7.7 Status of Submissions under Environmental Permits

The current status of submissions under the EP up to the reporting period is presented in **Table 7.9**.

Table 7.9: Status of Submissions under Environmental Permit

EP Condition	Submission	Status
2.1	Complaint Management Plan	Accepted / approved by EPD
2.4	Management Organizations	
2.5	Construction Works Schedule and Location Plans	
2.7	Marine Park Proposal	
2.8	Marine Ecology Conservation Plan	
2.9	Marine Travel Routes and Management Plan for Construction and Associated Vessels	
2.10	Marine Travel Routes and Management Plan for High Speed Ferries of SkyPier	
2.11	Marine Mammal Watching Plan	
2.12	Coral Translocation Plan	
2.13	Fisheries Management Plan	
2.14	Egret Survey Plan	
2.15	Silt Curtain Deployment Plan	
2.16	Spill Response Plan	
2.17	Detailed Plan on Deep Cement Mixing	
2.18	Landscape & Visual Plan	
2.19	Waste Management Plan	

EP Condition	Submission	Status
2.20	Supplementary Contamination Assessment Plan	
3.1	Updated EM&A Manual	
3.4	Baseline Monitoring Reports	

7.8 Compliance with Other Statutory Environmental Requirements

During the reporting period, environmental related licenses and permits required for the construction activities were checked. No non-compliance with environmental statutory requirements was recorded. The environmental licenses and permits which are valid in the reporting period are presented in **Appendix D**.

7.9 Analysis and Interpretation of Complaints, Notification of Summons and Status of Prosecutions

7.9.1 Complaints

A complaint regarding suspected dump truck for garbage disposal that was not properly covered and leaving the 3RS construction site area to landfill was received on 18 February 2022. The case was investigated by ET in accordance with the Manual and the Complaint Management Plan of the Project. The ET identified a related contractor and requested them to provide information. According to the reply, the contractor reported they had dump trucks for the disposal of garbage going to landfill by marine route during the period of investigation, stating their dump trucks were covered entirely and checked by site supervisors before leaving the construction site and that refresher trainings on the proper covering of dump trucks were provided to their dump truck drivers, site foremen and frontline workers. Based on the ET's weekly site inspections, no item related to the covering of dump trucks was recorded. Having said that, during an ad-hoc inspection by EPD, ET, IEC, and AAHK, some dump trucks were observed not fully covered when leaving the construction site onto RoRo barges. To follow up, ET reminded the related contractor to ensure their garbage is placed properly inside the skip of dump trucks and not to overfill the skips. The related contractor conducted their own checking of each dump truck to ensure all dump trucks were covered properly. ET would continue to monitor contractor's performance and reminded all 3RS contractors to ensure the proper covering of dump trucks for garbage disposal and avoid the potential blowing away of waste materials from their dump trucks. Hence, the case was considered closed.

7.9.2 Notifications of Summons or Status of Prosecution

Neither notification of summons nor prosecution was received during the reporting period.

7.9.3 Cumulative Statistics

Cumulative statistics on complaints, notifications of summons and status of prosecutions are summarised in **Appendix E**.

8 Future Key Issues and Other EIA & EM&A Issues

8.1 Construction Programme for the Coming Reporting Period

Key activities anticipated in the next reporting period for the Project will include the following:

Reclamation Works:

Contract 3206 Main Reclamation Works

- Seawall construction; and
- Backfilling works.

Airfield Works:

Contract 3301 North Runway Crossover Taxiway

- Cabling works; and
- Stockpiling.

Contract 3302 Eastern Vehicular Tunnel Advance Works

- Construction of tunnel structure;
- Pipe and drainage diversion works;
- Excavation and lateral support systems installation; and
- Stockpiling.

Contract 3303 Third Runway and Associated Works

- Architectural, Builder's and Finishing works;
- Footing and utilities work;
- Box culvert construction;
- Piling work;
- Operation of asphalt plant; and
- Cable laying and ducting works.

Contract 3305 Airfield Ground Lighting System

- Cabling works;
- Network installation; and
- Genset installation.

Contract 3306 Observation Facility Control System Supporting Interim 2RS and 3RS

- Equipment installation; and
- Installation of temporary site accommodation.

Contract 3307 Fire Training Facility

- Architectural, Builder's and Finishing works;
- Drainage and utilities works; and
- Building construction.

Contract 3308 Foreign Object Debris Detection System

- Foreign Object Debris Tower installation.

Contract 3310 North Runway Modification Works

- Excavation;
- Cutter soil mixing; and
- Deep cement mixing.

Third Runway Concourse

Contract 3403 New Integrated Airport Centres Building and Civil Works

- Architectural, Builder's Work and Finishing works;
- Road works;
- Cabling works; and
- Underground utilities construction.

Contract 3404 Integrated Airport Control System

- Equipment installation; and
- Cable laying.

Contract 3405 Third Runway Concourse Foundation and Substructure Works

- Sheet piling and bored piling;
- Excavation; and
- Road formation.

Contract 3408 Third Runway Concourse and Apron Works

- Site setup works; and
- Excavation and lateral support works.

Terminal 2 Expansion:

Contract 3508 Terminal 2 Expansion Works

- Excavation and footing construction;
- Bridge demolition;
- Block wall construction;
- Drainage works;
- Temporary road construction;
- TBM mobilization; and
- Architectural, Builder's Work and Finishing works.

Automated People Mover (APM) and Baggage Handling System (BHS):

Contract 3601 New Automated People Mover System (TRC Line)

- Guidebeam installation.

Contract 3602 Existing APM System Modification Works

- Car modification; and
- Concrete plinth and stitch construction.

Contract 3603 Baggage Handling System (BHS)

- BHS installation.

Construction Support (Facilities):

Contract 3721 Construction Support Infrastructure Works

- Laying of drainage pipes and ducts;
- Site clearance;
- Paving works; and
- Road works.

Contract 3723 Construction Support Facilities

- Clearance works;
- RC works; and
- Finishing works.

Airport Support Infrastructure:

Contract 3801 APM and BHS Tunnels on Existing Airport Island

- Excavation;
- Box jacking operation;
- Mass concreting; and
- Ventilation ducts construction.

Contract 3802 APM and BHS Tunnels and Related Works

- Fencing erection;
- Installation of dewatering well; and
- Excavation and lateral supports.

Construction Support (Services / Licenses):

Contract 3901A Concrete Batching Facility

- Operation of concrete batching plant; and
- Operation of conveyor belt.

Contract 3901B Concrete Batching Facility

- Operation of concrete batching plant; and
- Testing and commissioning for conveyor belt.

8.2 Key Environmental Issues for the Coming Reporting Period

The key environmental issues for the Project in the coming reporting period expected to be associated with the construction activities include:

- Generation of dust from construction works and stockpiles;
- Noise from operating equipment and machinery on-site;
- Generation of site surface runoffs and wastewater from activities on-site;
- Water quality from DCM works;
- DEZ monitoring for ground improvement works (DCM works) and seawall construction;
- Implementation of MMWP for silt curtain deployment;
- Sorting, recycling, storage and disposal of general refuse and construction waste;
- Reuse of treated marine sediments from piling and excavation works;
- Management of chemicals and avoidance of oil spillage on-site; and
- Acoustic decoupling measures for equipment on marine vessels.

The implementation of required mitigation measures by the contractors will be monitored by the ET.

8.3 Monitoring Schedule for the Coming Reporting Period

A tentative schedule of the planned environmental monitoring work in the next reporting period is provided in **Appendix B**.

8.4 Review of the Key Assumptions Adopted in the EIA Report

With reference to Appendix E of the Manual, it is noted that the key assumptions adopted in approved EIA report for the construction phase are still valid and no major changes are involved. The environmental mitigation measures recommended in the approved EIA Report remain applicable and shall be implemented in undertaking construction works for the Project.

9 Conclusion and Recommendation

The key activities of the Project carried out in the reporting period are located in reclamation areas and existing airport island respectively. Works in the reclamation areas included seawall construction, filling and ground improvement works, together with runway, concourse and associated works. Land-based works on existing airport island involved mainly airfield works, Terminal 2 expansion works, modification and tunnel work for Automated People Mover (APM) and Baggage Handling System (BHS), and preparation work for utilities, with activities include road and drainage works, cable ducting, demolition, piling, and excavation works.

All the monitoring works for construction dust, construction noise, water quality, construction waste, landscape & visual, and CWD were conducted during the reporting period in accordance with the Manual.

Monitoring results of construction dust, construction noise, water quality, and CWD did not trigger the corresponding Action and Limit Levels during the reporting period.

For waste management, a complaint regarding to general refuse was received in this reporting period. This complaint triggered the relevant Action Level, and the corresponding investigation was subsequently conducted in accordance with the Manual and the Complaint Management Plan of the Project. To conclude, follow-up actions have been made by ET and the related contractor and the case was considered closed.

Due to the COVID-19 pandemic, virtual and physical site inspections of the construction works to audit the implementation of proper environmental pollution control and mitigation measures for the Project were conducted by ET and IEC on a weekly and bi-weekly basis, respectively. Site inspection findings were recorded in the site inspection checklists and provided to the contractors to follow up.

On the implementation of the SkyPier Plan, due to the COVID-19 pandemic, all SkyPier HSF services to/from Zhuhai and Macau have been suspended from 25 March 2020 until further notice. No HSF movement between HKIA SkyPier and Zhuhai and Macau was recorded during the reporting period. Therefore, no deviation was recorded in the HSF monitoring in the reporting period. The daily movements of all SkyPier HSFs in the reporting period, including those not using the diverted route, were in the range of 3 to 4 daily movements, which are within the maximum daily cap of 125 daily movements.

On the implementation of MTRMP-CAV, the MSS automatically recorded the deviation case such as speeding, entering no entry zone and not travelling through the designated gates. ET conducted checking to ensure the MSS records all deviation cases accurately. Trainings have been provided for the concerned skippers to facilitate them in familiarising with the requirements of the MTRMP-CAV. Deviations including speeding in the works area, entered no entry zone, and entry from non-designated gates were reviewed by ET. All the concerned captains were reminded by the contractor's CTCC representative to comply with the requirements of the MTRMP-CAV. The ET reminded contractors that all vessels shall avoid entering the no-entry zone, in particular the Brothers Marine Park and the Sha Chau & Lung Kwu Chau Marine Park. Three-month rolling programmes for construction vessel activities, which ensures the proposed vessels are necessary and minimal through good planning, were also received from contractors.

Figures


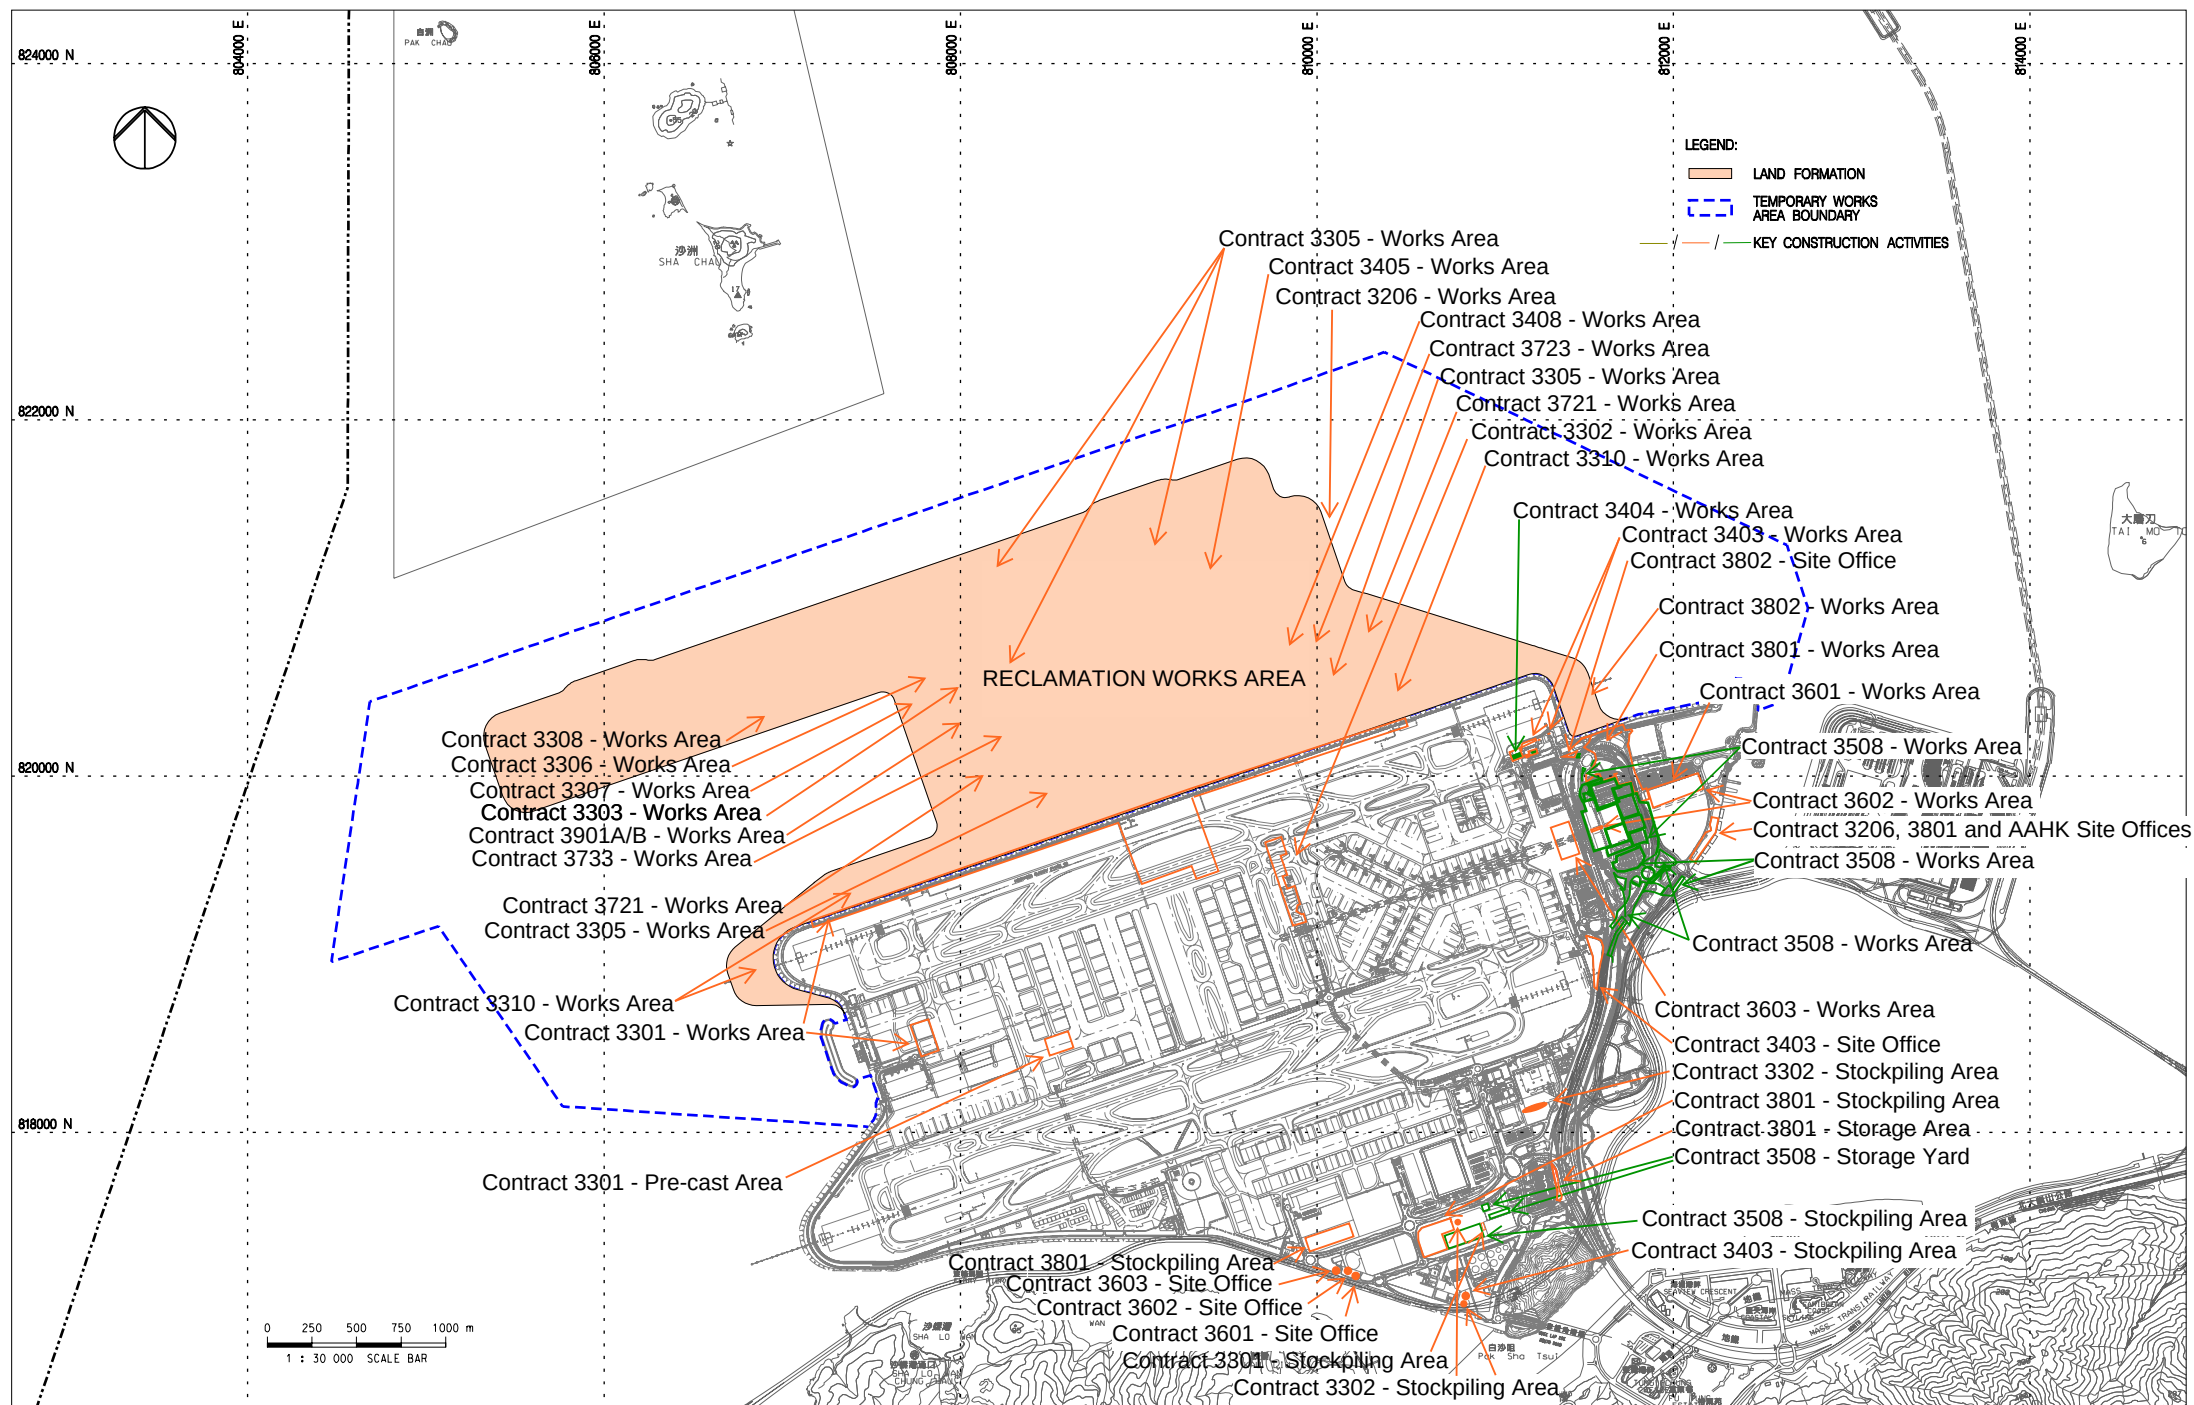


FIGURE 1.1 LOCATIONS OF KEY CONSTRUCTION ACTIVITIES

Note: The locations are for indicative purpose. The actual construction work locations are in accordance with the construction work programme.

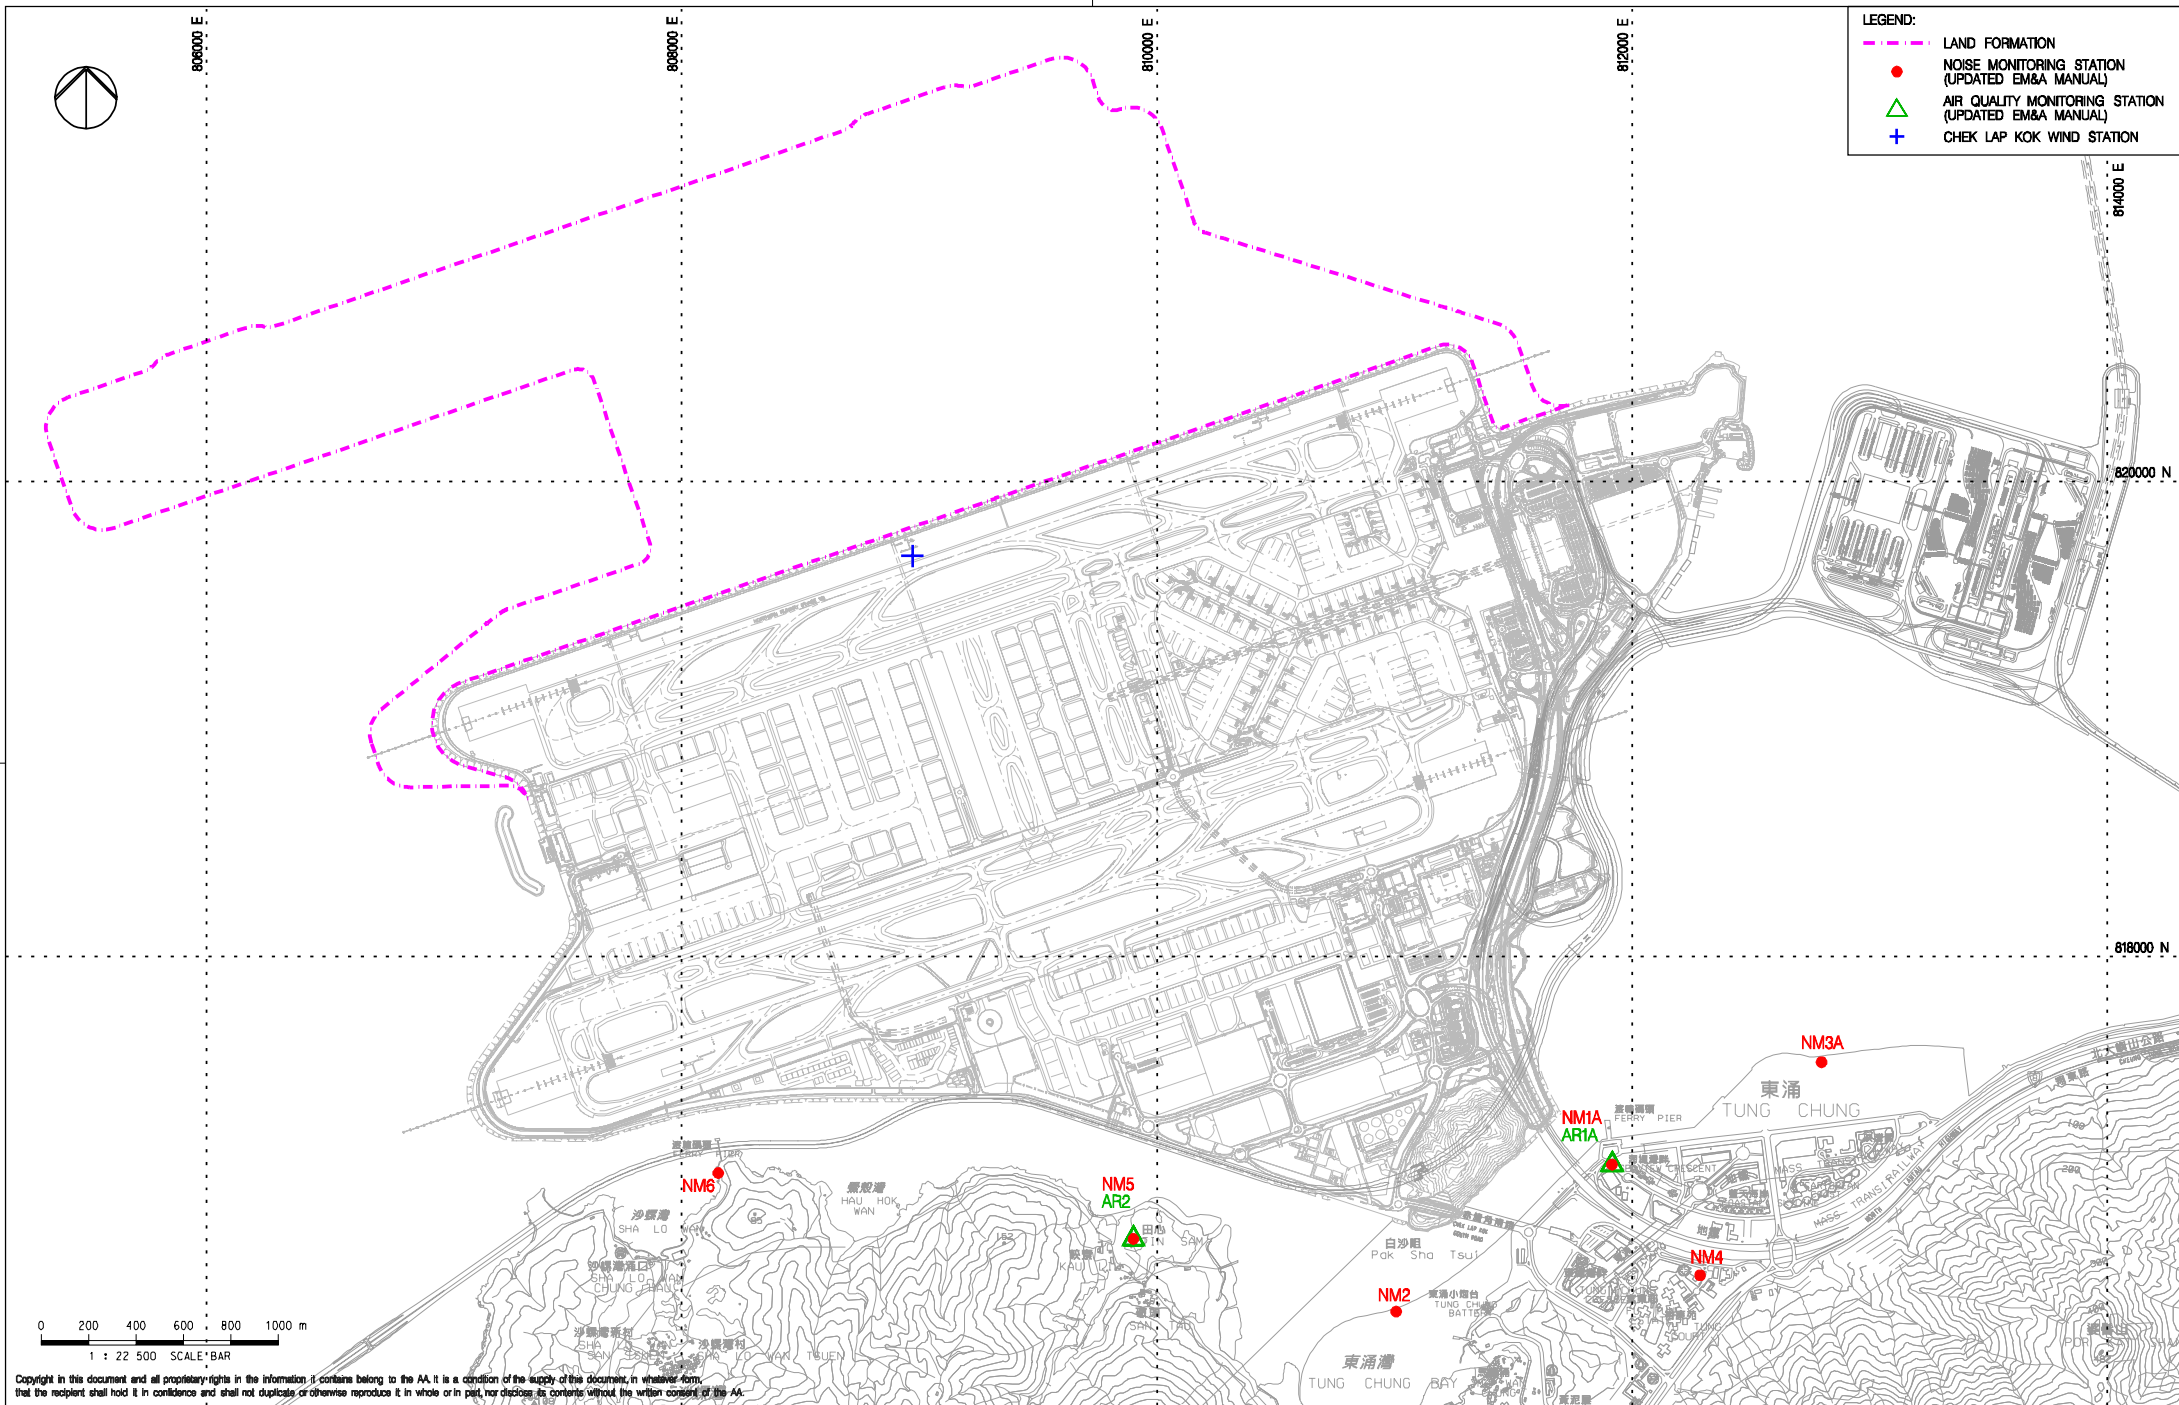

Copyright in this document and all proprietary rights in the information it contains belong to the AA. It is a condition of the supply of this document, in whatever form, that the recipient shall hold it in confidence and shall not duplicate or otherwise reproduce it in whole or in part, nor disclose its contents without the written consent of the AA.


Rev.	Date	Description	Checked
A	06JAN16	FIRST ISSUE	RO
B	29JAN16	GENERAL REVISION	RO
C	11FEB16	GENERAL REVISION	RO
D	29OCT18	GENERAL REVISION	SH



Title
LOCATIONS OF AIR AND NOISE MONITORING STATIONS AND CHEK LAP KOK WIND STATION

Consultant's Signatures for Approval		Date
Design	TK	29OCT18
Checkers	TK	29OCT18
Approver	EC	29OCT18

EXPANSION OF HONG KONG INTERNATIONAL AIRPORT INTO A THREE-RUNWAY SYSTEM		Scale at A3 1 : 22500
Drawing No.	FIGURE 2.1	Rev. D

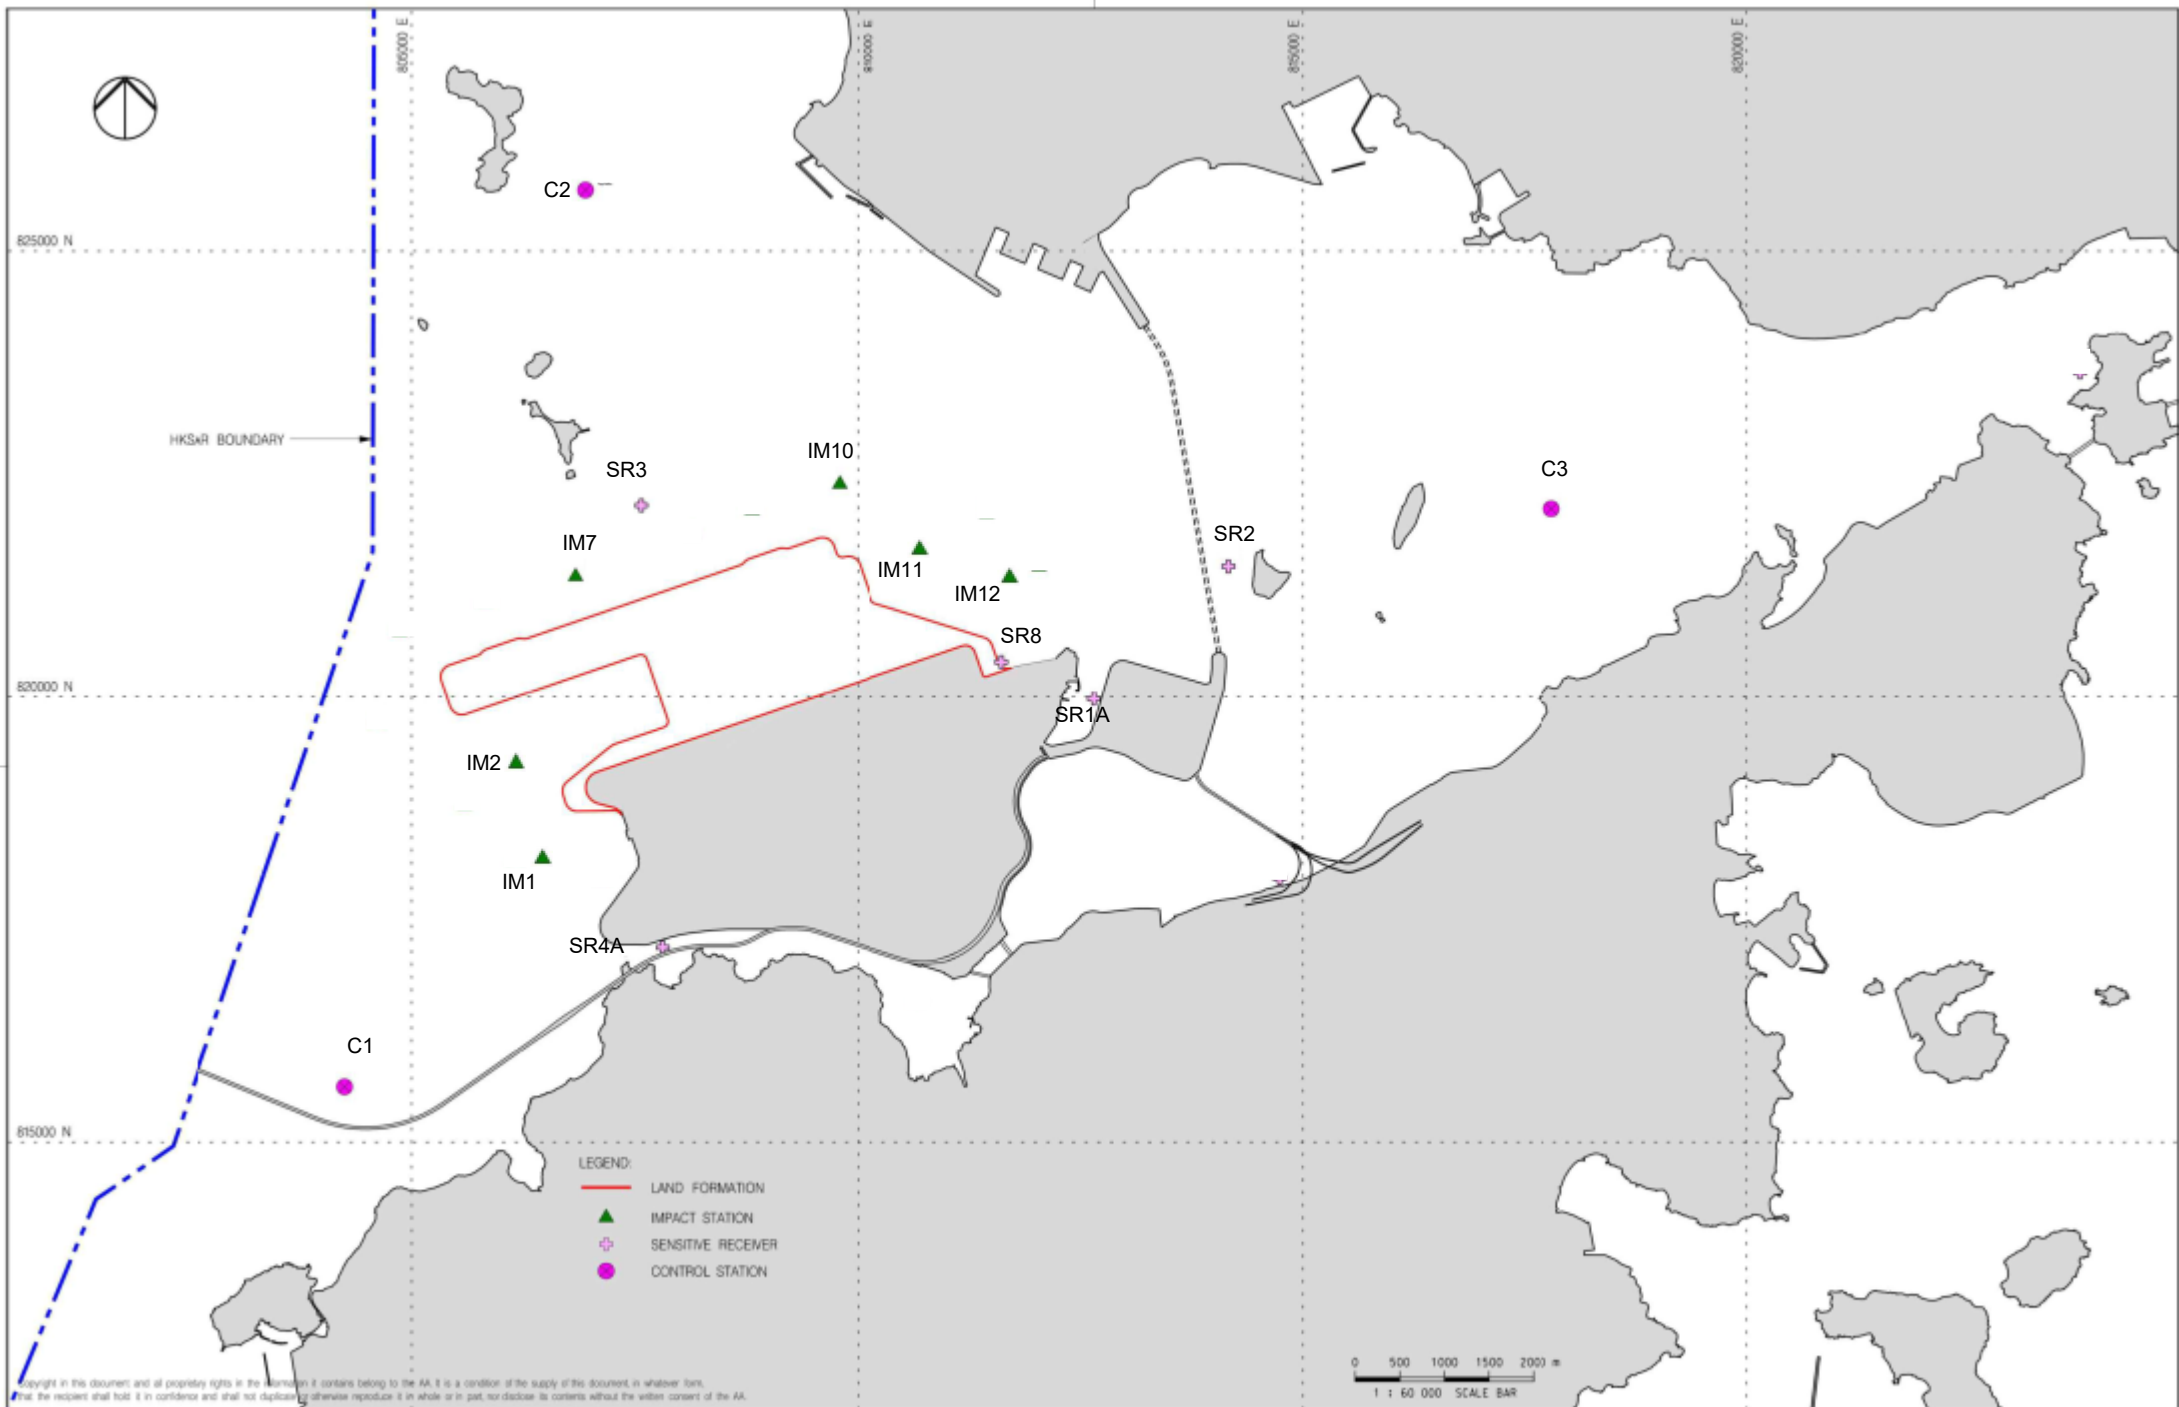

Copyright in this document and all proprietary rights in the information it contains belong to the AA. It is a condition of the supply of this document, in whatever form, that the recipient shall hold it in confidence and shall not duplicate or otherwise reproduce it in whole or in part, nor disclose its contents without the written consent of the AA.

Rev.	Date	Description	Checked
A	21AUG19	FIRST ISSUE	VL




Title

WATER QUALITY MONITORING STATIONS

Consultant's Signatures for Approval		Date
Design	DC	21AUG19
Checkers	DC / TK	21AUG19
Approver	EC	21AUG19

EXPANSION OF HONG KONG INTERNATIONAL AIRPORT INTO A THREE-RUNWAY SYSTEM		Scale at A3
Drawing No.	FIGURE 4.1	1 : 60000
Rev.	A	

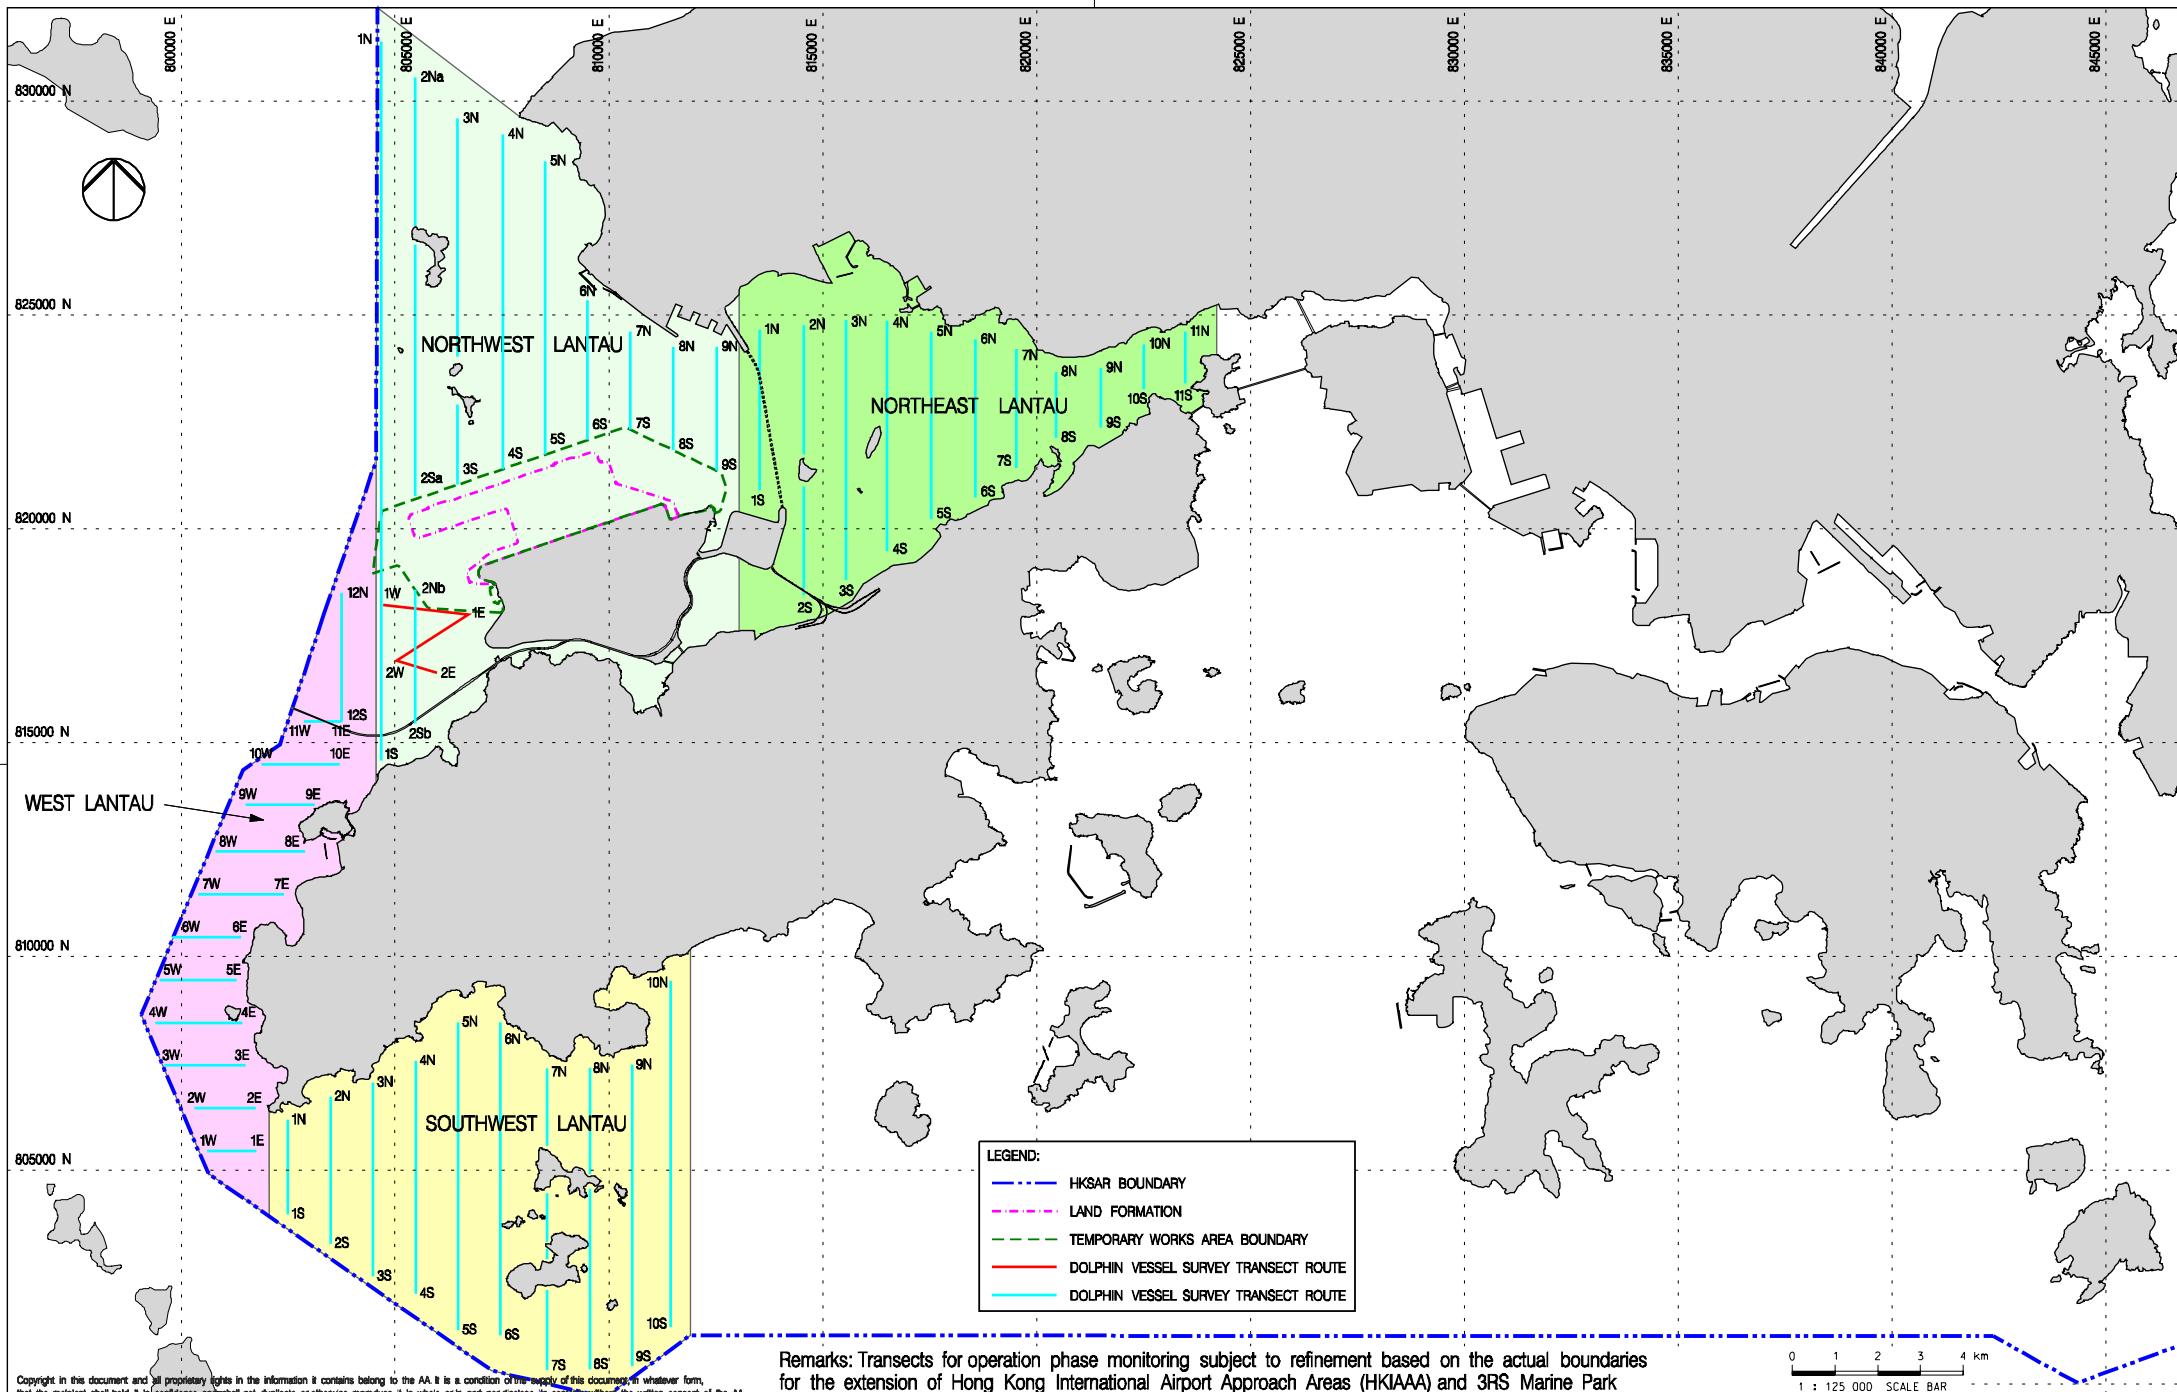

Copyright in this document and all proprietary rights in the information it contains belong to the AA. It is a condition of the supply of this document, in whatever form, that the recipient shall hold it in confidence and shall not duplicate or otherwise reproduce it in whole or in part, nor disclose its contents without the written consent of the AA.

Rev.	Date	Description	Checked
B	27JUL16	GENERAL REVISION	JT
C	06FEB17	GENERAL REVISION	JT
D	01MAR17	GENERAL REVISION	JT
E	29OCT18	GENERAL REVISION	SH
F	04APR19	GENERAL REVISION	SH





Title

VESSEL BASED DOLPHIN MONITORING
TRANSECTS IN CONSTRUCTION,
POST-CONSTRUCTION AND OPERATION PHASES

Consultant's Signatures for Approval		Date
Design	JC	04APR19
Checkers	JC / TK	04APR19
Approver	EC	04APR19

EXPANSION OF HONG KONG INTERNATIONAL AIRPORT INTO A THREE-RUNWAY SYSTEM		Scale at A3 1 : 125000
Drawing No.	FIGURE 6.1	Rev. F



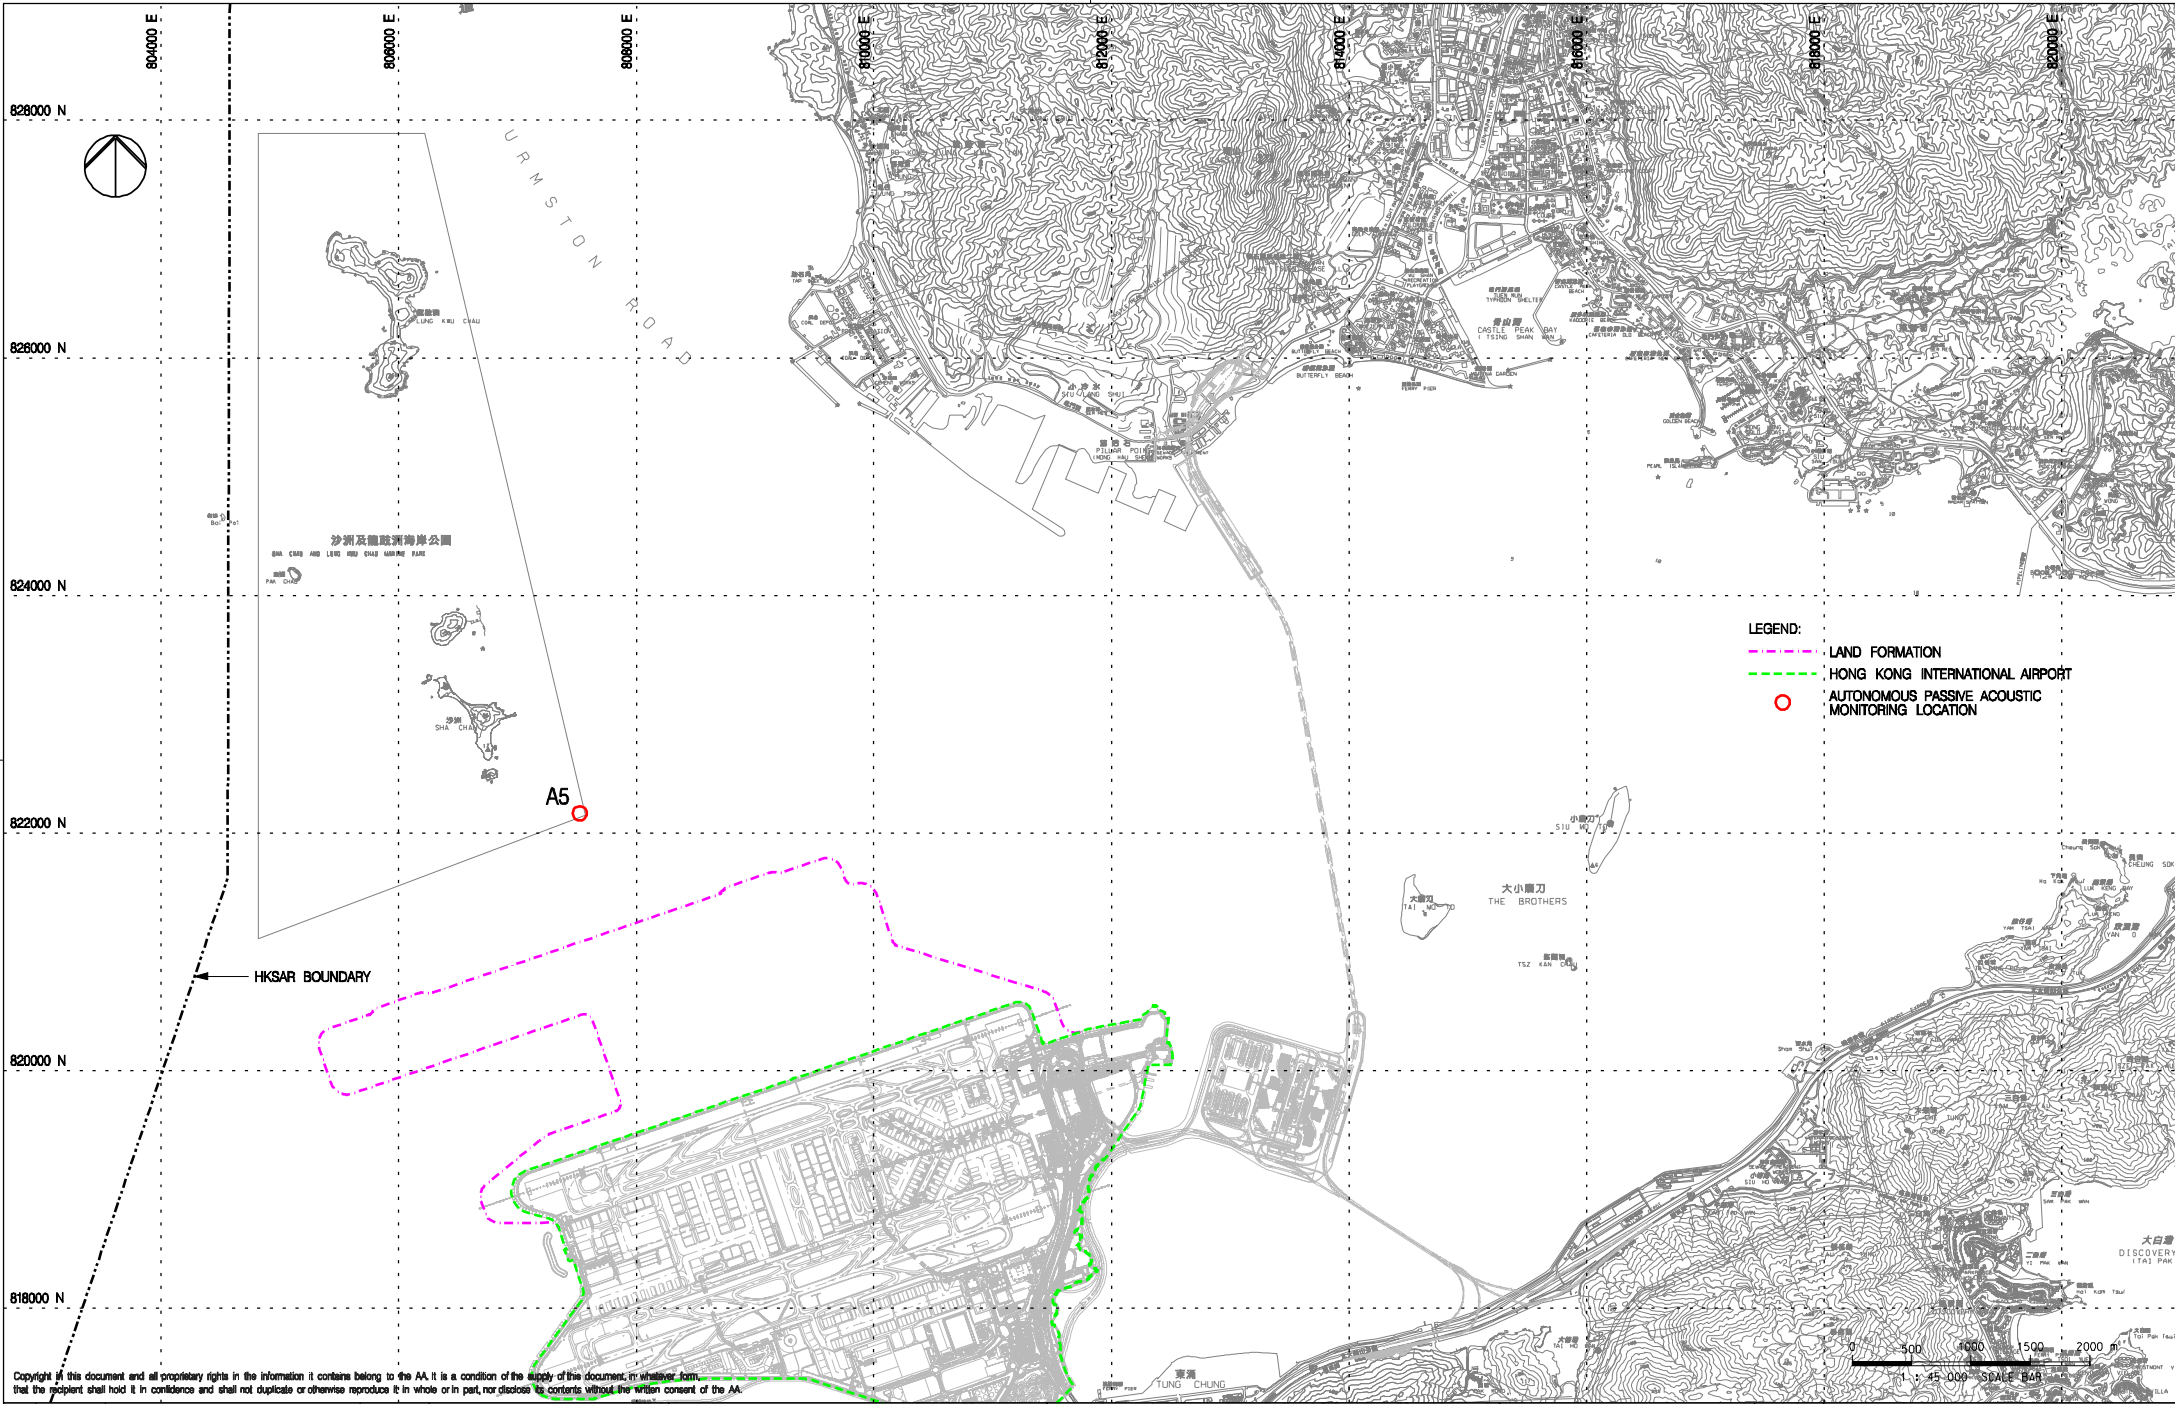

Copyright in this document and all proprietary rights in the information it contains belong to the AA. It is a condition of the supply of this document, in whatever form, that the recipient shall hold it in confidence and shall not duplicate or otherwise reproduce it in whole or in part, nor disclose its contents without the written consent of the AA.

Rev.	Date	Description	Checked
A	29AUG17	FIRST ISSUE	JT
B	10OCT17	GENERAL REVISION	PL
C	29OCT18	GENERAL REVISION	SH



Title
LOCATION FOR AUTONOMOUS PASSIVE
ACOUSTIC MONITORING

Consultant's Signatures for Approval		Date
Design	JC	29OCT18
Checkers	JC / TK	29OCT18
Approver	EC	29OCT18

EXPANSION OF HONG KONG INTERNATIONAL AIRPORT INTO A THREE-RUNWAY SYSTEM	
Drawing No.	
FIGURE 6.5	
Scale at A3 1:45000	Rev. C

Appendix A. Environmental Mitigation Implementation Schedule (EMIS) for Construction Phase

Environmental Mitigation Implementation Schedule (EMIS) for Construction Phase

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
Air Quality Impact – Construction Phase					
5.2.6.2	2.1	-	Dust Control Measures Water spraying for 12 times a day or once every two hours for 24-hour working at all active works area.	Within construction site / Duration of the construction phase	I
5.2.6.3	2.1	-	Covering of at least 80% of the stockpiling area by impervious sheets. Water spraying of all dusty materials immediately prior to any loading transfer operation so as to keep the dusty material wet during material handling.	Within construction site / Duration of the construction phase	I
5.2.6.4	2.1	-	Dust control practices as stipulated in the Air Pollution Control (Construction Dust) Regulation should be adopted. These practices include: Good Site Management Good site management is important to help reducing potential air quality impact down to an acceptable level. As a general guide, the Contractor should maintain high standard of housekeeping to prevent emission of fugitive dust. Loading, unloading, handling and storage of raw materials, wastes or by-products should be carried out in a manner so as to minimise the release of visible dust emission. Any piles of materials accumulated on or around the work areas should be cleaned up regularly. Cleaning, repair and maintenance of all plant facilities within the work areas should be carried out in a manner minimising generation of fugitive dust emissions. The material should be handled properly to prevent fugitive dust emission before cleaning.	Within construction site / Duration of the construction phase	I
			Disturbed Parts of the Roads - Each and every main temporary access should be paved with concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials; or - Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet.	Within construction site / Duration of the construction phase	I
			Exposed Earth Exposed earth should be properly treated by compaction, hydroseeding, vegetation planting or seating with latex, vinyl, bitumen within six months after the last construction activity on the site or part of the site where the exposed earth lies.	Within construction site / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Loading, Unloading or Transfer of Dusty Materials All dusty materials should be sprayed with water immediately prior to any loading or transfer operation so as to keep the dusty material wet.	Within construction site / Duration of the construction phase	I
			Debris Handling - Any debris should be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the three sides; and - Before debris is dumped into a chute, water should be sprayed so that it remains wet when it is dumped.	Within construction site / Duration of the construction phase	I
			Transport of Dusty Materials Vehicle used for transporting dusty materials/spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards.	Within construction site / Duration of the construction phase	I
			Wheel washing Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels.	Within construction site / Duration of the construction phase	I
			Use of vehicles - The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site; - Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels; and - Where a vehicle leaving the construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle.	Within construction site / Duration of the construction phase	I
			Site hoarding Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit.	Within construction site / Duration of the construction phase	I
5.2.6.5	2.1	-	Best Practices for Concrete Batching Plant The relevant best practices for dust control as stipulated in the Guidance Note on the Best Practicable Means for Cement Works (Concrete Batching Plant) BPM 3/2 as well as in the future Specified Process licence should be adopted. The best practices are recommended to be applied to both the land based and floating concrete batching plants. Best practices include: Cement and other dusty materials	Within Concrete Batching Plant / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- The loading, unloading, handling, transfer or storage of cement, pulverised fuel ash (PFA) and/or other equally dusty materials shall be carried in a totally enclosed system acceptable to EPD. All dust-laden air or waste gas generated by the process operations shall be properly extracted and vented to fabric filtering system to meet the required emission limit; - Cement, PFA and/or other equally dusty materials shall be stored in storage silo fitted with audible high-level alarms to warn of over-filling. The high-level alarm indicators shall be interlocked with the material filling line such that in the event of the silo approaching an overfilling condition, an audible alarm will operate, and after 1 minute or less the material filling line will be closed; - Vents of all silos shall be fitted with fabric filtering system to meet the required emission limit; - Vents of cement/PFA weighing scale shall be fitted with fabric filtering system to meet the required emission limit; and - Seating of pressure relief valves of all silos shall be checked, and the valves re-seated if necessary, before each delivery.		
			Other raw materials - The loading, unloading, handling, transfer or storage of other raw materials which may generate airborne dust emissions such as crushed rock, sand, stone aggregate, shall be carried out in such a manner to prevent or minimize dust emissions; - The materials shall be adequately wetted prior to and during the loading, unloading and handling operations. Manual or automatic water spraying system shall be provided at all unloading areas, stockpiles and material discharge points; - All receiving hoppers for unloading relevant materials shall be enclosed on three sides up to 3 m above the unloading point. In no case shall these hoppers be used as the material storage devices; - The belt conveyor for handling materials shall be enclosed on top and two sides with a metal board at the bottom to eliminate any dust emission due to wind-whipping effect. Other type of enclosure will also be accepted by EPD if it can be demonstrated that the proposed enclosure can achieve same performance; - All conveyor transfer points shall be totally enclosed. Openings for the passage of conveyors shall be fitted with adequate flexible seals; - Scrapers shall be provided at the turning points of all conveyors to remove dust adhered to the belt surface; - Conveyors discharged to stockpiles of relevant materials shall be arranged to minimize free fall as far as practicable. All free falling transfer points from conveyors to stockpiles shall be enclosed with chute(s) and water sprayed; - Aggregates with a nominal size less than or equal to 5 mm should be stored in totally enclosed structure such as storage bin and should not be handled in open area. Where there is sufficient buffer area surrounding the concrete batching plant, ground stockpiling may be used;	Within Concrete Batching Plant / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- The stockpile shall be enclosed at least on top and three sides and with flexible curtain to cover the entrance side; - Aggregates with a nominal size greater than 5 mm should preferably be stored in a totally enclosed structure. If open stockpiling is used, the stockpile shall be enclosed on three sides with the enclosure wall sufficiently higher than the top of the stockpile to prevent wind whipping; and - The opening between the storage bin and weighing scale of the materials shall be fully enclosed.		
			Loading of materials for batching - Concrete truck shall be loaded in such a way as to minimise airborne dust emissions. The following control measures shall be implemented: - Pre-mixing the materials in a totally enclosed concrete mixer before loading the materials into the concrete truck is recommended. All dust-laden air generated by the pre-mixing process as well as the loading process shall be totally vented to fabric filtering system to meet the required emission limit; and - If truck mixing batching or other types of batching method is used, effective dust control measures acceptable to EPD shall be adopted. The dust control measures must have been demonstrated to EPD that they are capable to collect and vent all dust-laden air generated by the material loading/mixing to dust arrestment plant to meet the required emission limit. - The loading bay shall be totally enclosed during the loading process.	Within Concrete Batching Plant / Duration of the construction phase	I
			Vehicles - All practicable measures shall be taken to prevent or minimize the dust emission caused by vehicle movement; and - All access and route roads within the premises shall be paved and adequately wetted.	Within Concrete Batching Plant / Duration of the construction phase	I
			Housekeeping A high standard of housekeeping shall be maintained. All spillages or deposits of materials on ground, support structures or roofs shall be cleaned up promptly by a cleaning method acceptable to EPD. Any dumping of materials at open area shall be prohibited.	Within Concrete Batching Plant / Duration of the construction phase	I
5.2.6.6	2.1	-	Best Practices for Asphaltic Concrete Plant The relevant best practices for dust control as stipulated in the Guidance Note on the Best Practicable Means for Tar and Bitumen Works (Asphaltic Concrete Plant) BPM 15 (94) as well as in the future Specified Process licence should be adopted. These include: Design of Chimney - The chimney shall not be less than 3 metres plus the building height or 8 metres above ground level, whichever is the greater; - The efflux velocity of gases from the main chimney shall not be less than 12 m/s at full load condition;	Within Concrete Batching Plant / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- The flue gas exit temperature shall not be less than the acid dew point; and - Release of the chimney shall be directed vertically upwards and not be restricted or deflected.		
			Cold feed side - The aggregates with a nominal size less than or equal to 5 mm shall be stored in totally enclosed structure such as storage bin and shall not be handled in open area; - Where there is sufficient buffer area surrounding the plant, ground stockpiling may be used. The stockpile shall be enclosed at least on top and three sides and with flexible curtain to cover the entrance side. If these aggregates are stored above the feeding hopper, they shall be enclosed at least on top and three sides and be wetted on the surface to prevent wind-whipping; - The aggregates with a nominal size greater than 5 mm should preferably be stored in totally enclosed structure. Aggregates stockpile that is above the feeding hopper shall be enclosed at least on top and three sides. If open stockpiling is used, the stockpiles shall be enclosed on three sides with the enclosure wall sufficiently higher than the top of the stockpile to prevent wind whipping; - Belt conveyors shall be enclosed on top and two sides and provided with a metal board at the bottom to eliminate any dust emission due to the wind-whipping effect. Other type of enclosure will also be accepted by EPD if it can be demonstrated that the proposed enclosure can be achieve the same performance; - Scrapers shall be provided at the turning points of all belt conveyors inside the chute of the transfer points to remove dust adhered to the belt surface; - All conveyor transfer points shall be totally enclosed. Openings for the passages of conveyors shall be fitted with adequate flexible seals; and - All materials returned from dust collection system shall be transferred in enclosed system and shall be stored inside bins or enclosures.	Within Concrete Batching Plant / Duration of the construction phase	I
			Hot feed side - The inlet and outlet of the rotary dryer shall be enclosed and ducted to a dust extraction and collection system such as a fabric filter. The particulate and gaseous concentration at the exhaust outlet of the dust collector shall not exceed the required limiting values; - The bucket elevator shall be totally enclosed and the air be extracted and ducted to a dust collection system to meet the required particulates limiting value; - All vibratory screens shall be totally enclosed and dust tight with close-fitted access inspection opening. Gaskets shall be installed to seal off any cracks and edges of any inspection openings; - Chutes for carrying hot material shall be rigid and preferably fitted with abrasion resistant plate inside. They shall be inspected daily for leakages; - All hot bins shall be totally enclosed and dust tight with close-fitted access inspection opening. Gaskets shall be installed to seal off any cracks and edges of any inspection openings. The air shall be extracted and ducted to a dust collection system to meet the required particulates limiting value; and	Within Concrete Batching Plant / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Appropriate control measures shall be adopted in order to meet the required bitumen emission limit as well as the ambient odour level (2 odour units).		
			Material transportation - The loading, unloading, handling, transfer or storage of other raw materials which may generate airborne dust emissions such as crushed rocks, sands, stone aggregates, reject fines, shall be carried out in such a manner as to minimize dust emissions; - Roadways from the entrance of the plant to the product loading points and/or any other working areas where there are regular movements of vehicles shall be paved or hard surfaced; and - Haul roads inside the Works shall be adequately wetted with water and/or chemical suppressants by water trucks or water sprayers.	Within Concrete Batching Plant / Duration of the construction phase	I
			Control of emissions from bitumen decanting - The heating temperature of the particular bitumen type and grade shall not exceed the corresponding temperature limit of the same type listed in Appendix 1 of the Guidance Note; - Tamper-free high temperature cut-off device shall be provided to shut off the fuel supply or electricity in case the upper limit for bitumen temperature is reached; - Proper chimney for the discharge of bitumen fumes shall be provided at high level; - The emission of bitumen fumes shall not exceed the required emission limit; and - The air-to-fuel ratio shall be properly controlled to allow complete combustion of the fuel. The fuel burners, if any, shall be maintained properly and free from carbon deposits in the burner nozzles.	Within Concrete Batching Plant / Duration of the construction phase	I
			Liquid fuel The receipt, handling and storage of liquid fuel shall be carried out so as to prevent the release of emissions of organic vapours and/or other noxious and offensive emissions to the air.	Within Concrete Batching Plant / Duration of the construction phase	I
			Housekeeping A high standard of housekeeping shall be maintained. Waste material, spillage and scattered piles gathered beneath belt conveyors, inside and around enclosures shall be cleared frequently. The minimum clearing frequency is on a weekly basis.	Within Concrete Batching Plant / Duration of the construction phase	I
5.2.6.7	2.1	-	Best Practices for Rock Crushing Plants The relevant best practices for dust control as stipulated in the Guidance Note on the Best Practicable Means for Mineral Works (Stone Crushing Plant) BPM 11/1 (95) as well as in the future Specified Process licence should be adopted. These include: Crushers	Within Concrete Batching Plant / Duration of the construction phase	N/A as there was no rock crushing plant at this stage

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			▪ The outlet of all primary crushers, and both inlet and outlet of all secondary and tertiary crushers, if not installed inside a reasonably dust tight housing, shall be enclosed and ducted to a dust extraction and collection system such as a fabric filter; ▪ The inlet hopper of the primary crushers shall be enclosed on top and 3 sides to contain the emissions during dumping of rocks from trucks. The rock while still on the trucks shall be wetted before dumping; ▪ Water sprayers shall be installed and operated in strategic locations at the feeding inlet of crushers; and ▪ Crusher enclosures shall be rigid and be fitted with self-closing doors and close-fitting entrances and exits. Where conveyors pass through the crusher enclosures, flexible covers shall be installed at entries and exits of the conveyors to the enclosure.		
			Vibratory screens and grizzlies ▪ All vibratory screens shall be totally enclosed in a housing. Screenhouses shall be rigid and reasonably dust tight with self-closing doors or close-fitted entrances and exits for access. Where conveyors pass through the screenhouse, flexible covers shall be installed at entries and exits of the conveyors to the housing. Where containment of dust within the screenhouse structure is not successful then a dust extraction and collection system shall be provided; and ▪ All grizzlies shall be enclosed on top and 3 sides and sufficient water sprayers shall be installed at their feeding and outlet areas.	Within Concrete Batching Plant / Duration of the construction phase	N/A as there was no rock crushing plant at this stage
			Belt conveyors ▪ Except for those conveyors which are placed within a totally enclosed structure such as a screenhouse or those erected at the ground level, all conveyors shall be totally enclosed with windshield on top and 2 sides; ▪ Effective belt scraper such as the pre-cleaner blades made by hard wearing materials and provided with pneumatic tensioner, or equivalent device, shall be installed at the head pulley of designated conveyor as required to dislodge fine dust particles that may adhere to the belt surface and to reduce carry-back of fine materials on the return belt. Bottom plates shall also be provided for the conveyor unless it has been demonstrated that the corresponding belt scraper is effective and well maintained to prevent falling material from the return belt; and Except for those transfer points which are placed within a totally enclosed structure such as a screenhouse, all transfer points to and from conveyors shall be enclosed. Where containment of dust within the enclosure is not successful, then water sprayers shall be provided. Openings for any enclosed structure for the passage of conveyors shall be fitted with flexible seals.	Within Concrete Batching Plant / Duration of the construction phase	N/A as there was no rock crushing plant at this stage
			Storage piles and bins ▪ Where practicable, free falling transfer points from conveyors to stockpiles shall be fitted with flexible curtains or be enclosed with chutes designed to minimize the drop height. Water sprays shall also be used where required.	Within Concrete Batching Plant / Duration of the construction phase	N/A as there was no rock crushing plant at this stage

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- The surface of all surge piles and stockpiles of blasted rocks or aggregates shall be kept sufficiently wet by water spraying wherever practicable; - All open stockpiles for aggregates of size in excess of 5 mm shall be kept sufficiently wet by water spraying where practicable; or - The stockpiles of aggregates 5 mm in size or less shall be enclosed on 3 sides or suitably located to minimize wind-whipping. Save for fluctuations in stock or production, the average stockpile shall stay within the enclosure walls and in no case the height of the stockpile shall exceed twice the height of the enclosure walls; and - Scattered piles gathered beneath belt conveyors, inside and around enclosures shall be cleared regularly.		
			Rock drilling equipment Appropriate dust control equipment such as a dust extraction and collection system shall be used during rock drilling activities.	Within Concrete Batching Plant / Duration of the construction phase	N/A as there was no rock crushing plant at this stage
Hazard to Human Life – Construction Phase					
Table 6.40	3.2	-	Precautionary measures should be established to request barges to move away during typhoons.	Construction Site / Construction Period	I
Table 6.40	3.2	-	An appropriate marine traffic management system should be established to minimize risk of ship collision.	Construction Site / Construction Period	I
Table 6.40	3.2	-	Location of all existing hydrant networks should be clearly identified prior to any construction works.	Construction Site / Construction Period	I
Noise Impact – Construction Phase					
7.5.6	4.3	-	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during each phase of construction: - only well-maintained plant to be operated on-site and plant should be serviced regularly during the construction works; - machines and plant that may be in intermittent use to be shut down between work periods or should be throttled down to a minimum; - plant known to emit noise strongly in one direction, should, where possible, be orientated to direct noise away from the NSRs; - mobile plant should be sited as far away from NSRs as possible; and - material stockpiles and other structures to be effectively utilised, where practicable, to screen noise from on-site construction activities.	Within the Project site / During construction phase / Prior to commencement of operation	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
7.5.6	4.3	-	Adoption of QPME QPME should be adopted as far as applicable.	Within the Project site / During construction phase / Prior to commencement of operation	I
7.5.6	4.3	-	Use of Movable Noise Barriers Movable noise barriers should be placed along the active works area and mobile plants to block the direct line of sight between PME and the NSRs.	Within the Project site / During construction phase / Prior to commencement of operation	I
7.5.6	4.3	-	Use of Noise Enclosure/ Acoustic Shed Noise enclosure or acoustic shed should be used to cover stationary PME such as air compressor and generator.	Within the Project site / During construction phase / Prior to commencement of operation	I
Water Quality Impact – Construction Phase					
8.8.1.2 and 8.8.1.3	5.1	2.26	Marine Construction Activities <u>General Measures to be Applied to All Works Areas</u> - Barges or hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation; - Use of Lean Material Overboard (LMOB) systems shall be prohibited; - Excess materials shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessels are moved; - Plants should not be operated with leaking pipes and any pipe leakages shall be repaired quickly; - Adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; - All vessels shall be sized such that adequate clearance is maintained between vessels and the seabed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; - The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site; and - For ground improvement activities including DCM, the wash water from cleaning of the drilling shaft should be appropriately treated before discharge. The Contractor should ensure the wastewater meets the WPCO/TM requirements before discharge. No direct discharge of contaminated water is permitted.	Within construction site / Duration of the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			<u>Specific Measures to be Applied to All Works Areas</u> - The daily maximum production rates shall not exceed those assumed in the water quality assessment in the EIA report; - A maximum of 10 % fines content to be adopted for sand blanket and 20 % fines content for marine filling below +2.5 mPD prior to substantial completion of seawall (until end of Year 2017) shall be specified in the works contract document;	Within construction site / Duration of the construction phase	I – For marine filling
			An advance seawall of at least 200m to be constructed (comprising either rows of contiguous permanent steel cells completed above high tide mark or partially completed seawalls with rock core to high tide mark and filter layer on the inner side) prior to commencement of marine filling activities;		C – Completed in Nov 2020 for sand blanket
			- Closed grab dredger shall be used to excavate marine sediment; - Silt curtains surrounding the closed grab dredger shall be deployed in accordance with the Silt Curtain Deployment Plan; and		I (The arrangement of silt curtain has been modified. The details can be referred to Silt Curtain Deployment Plan)
			The Silt Curtain Deployment Plan shall be implemented.		I
			<u>Specific Measures to be Applied to Land Formation Activities prior to Commencement of Marine Filling Works</u> Double layer 'Type III' silt curtains to be applied around the active eastern works areas prior to commencement of sand blanket laying activities. The silt curtains shall be configured to minimise SS release during ebb tides. A silt curtain efficiency test shall be conducted to validate the performance of the silt curtains;	Within construction site / Duration of the construction phase	N/A (The arrangement of silt curtain has been modified. The details can be referred to Silt Curtain Deployment Plan)
			Double layer silt curtains to enclose WSRs C7a and silt screens installed at the intake points for both WSR C7a and C8 prior to commencement of construction; and		I – For C7a
					C – Completed in Dec 2021 for C8 *(The requirement of silt curtain / screen has been modified. The details can be referred to Silt Curtain Deployment Plan)
			The silt curtains and silt screens should be regularly checked and maintained.		I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			<u>Specific Measures to be Applied to Land Formation Activities during Marine Filling Works</u> Double layer 'Type II' or 'Type III' silt curtains to be applied around the eastern openings between partially completed seawalls prior to commencement of marine filling activities. The silt curtains shall be configured to minimise SS release during ebb tides;	Within construction site / Duration of the construction phase	I *(The arrangement of silt curtain has been modified. The details can be referred to Silt Curtain Deployment Plan)
			Double layer silt curtains to be applied at the south-western opening prior to commencement of marine filling activities;		N/A (The arrangement of silt curtain has been modified. The details can be referred to Silt Curtain Deployment Plan)
			Double layer silt curtain to enclose WSR C7a and silt screens installed at the intake points for both WSR C7a and C8 prior to commencement of marine filling activities; and		I – For C7a C – Completed in Dec 2021 for C8 (The requirement of silt curtain / screen has been modified. The details can be referred to Silt Curtain Deployment Plan)
			The silt curtains and silt screens should be regularly checked and maintained.		I
			<u>Specific Measures to be Applied to the Field Joint Excavation Works for the Submarine Cable Diversion</u> - Only closed grabs designed and maintained to avoid spillage shall be used and should seal tightly when operated. Excavated materials shall be disposed at designated marine disposal area in accordance with the Dumping at Sea Ordinance (DASO) permit conditions; and - Silt curtains surrounding the closed grab dredger to be deployed as a precautionary measure.	Within construction site / Duration of the construction phase	N/A – the field joint excavation works for the submarine cable diversion will no longer be conducted anymore
8.8.1.4	5.1	-	Modification of the Existing Seawall Silt curtains shall be deployed around the seawall modification activities to completely enclose the active works areas, and care should be taken to avoid splashing of rockfill / rock armour into the surrounding marine environment. For the connecting sections with the existing outfalls, works for these connection areas should be undertaken during the dry season in order that individual drainage culvert cells may be isolated for interconnection works.	At the existing northern seawall / Duration of the construction phase	I

12

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly;		I
			Measures should be taken to minimize the ingress of site drainage into excavations. If excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities;		I
			In the event that contaminated groundwater is identified at excavation areas, this should be treated on-site using a suitable wastewater treatment process. The effluent should be treated according to the requirements of the TM-DSS standards under the WPCO prior to discharge to foul sewers or collected for proper disposal off-site. No direct discharge of contaminated groundwater is permitted; and		I
			All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facility should be provided at construction site exits. Wash-water should have sand and silt settled out and removed regularly to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. All washwater should be treated according to the requirements of the TM-DSS standards under the WPCO prior to discharge.		I
			Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the construction materials, soil, silt or debris from washing away into the drainage system;		I
			Manholes (including newly constructed ones) should be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and to prevent stormwater runoff being directed into foul sewers; and		I
			Precautionary measures should be taken at any time of the year when rainstorms are likely. Actions to be taken when a rainstorm is imminent or forecasted are summarized in Appendix A2 of ProPECC Note PN 1/94. This includes actions to be taken during and/or after rainstorms. Particular attention should be paid to the control of silty surface runoff during storm events.		I
8.8.1.9	5.1	-	Sewage Effluent from Construction Workforce Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	Within construction site / During construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
8.8.1.10 8.8.1.11	5.1		General Construction Activities - Construction solid waste, debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby storm water drain. Stockpiles of cement and other construction materials should be kept covered when not being used; and - Oils and fuels should only be stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to any nearby storm water drain, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event.	Within construction site / During construction phase	I
8.8.1.12 8.8.1.13	5.1	2.28	Drilling Activities for the Submarine Aviation Fuel Pipelines To prevent potential water quality impacts at Sha Chau, the following measures shall be applied: - A 'zero-discharge' policy shall be applied for all activities to be conducted at Sha Chau; - No bulk storage of chemicals shall be permitted; and - A containment pit shall be constructed around the drill holes. This containment pit shall be lined with impermeable lining and bunded on the outside to prevent inflow from off-site areas.	Within construction site / During construction phase	C – Completed in Jan 2019
			At the airport island side of the drilling works, the following measures shall be applied for treatment of wastewater: - During pipe cleaning, appropriate desilting or sedimentation device should be provided on site for treatment before discharge. The Contractor should ensure discharge water from the sedimentation tank meet the WPCO/TM requirements before discharge; and - Drilling fluid used in drilling activities should be reconditioned and reused as far as possible. Temporary enclosed storage locations should be provided on-site for any unused chemicals that needs to be transported away after all the related construction activities are completed. The requirements in ProPECC Note PN 1/94 should be adhered to in the handling and disposal of bentonite slurries.	Within construction site / During construction phase	C – Completed in Jan 2019
Waste Management Implication – Construction Phase					
10.5.1.1	7.1	-	Opportunities to minimise waste generation and maximise the reuse of waste materials generated by the project have been incorporated where possible into the planning, design and construction stages, and the following measures have been recommended: - The relevant construction methods (particularly for the tunnel works) and construction programme have been carefully planned and developed to minimise the extent of excavation and to maximise the on-site reuse of inert C&D materials generated by the project as far as practicable. Temporary stockpiling areas will also be provided to facilitate on-site reuse of inert C&D materials; - Priority should be given to collect and reuse suitable inert C&D materials generated from other concurrent projects and the Government's PFRF as fill materials for the proposed land formation works;	Project Site Area / During design and construction phase	I
					I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Only non-dredged ground improvement methods should be adopted in order to completely avoid the need for dredging and disposal of marine sediment for the proposed land formation work;		I
			Excavation work for constructing the APM tunnels, BHS tunnels and airside tunnels will not be down to the CMPs beneath the fill materials in order to avoid excavating any sediments; and		I
			For the marine sediments expected to be excavated from the piling works of TRC, APM & BHS tunnels, airside tunnels and other facilities on the proposed land formation area, piling work of marine sections of the approach lights and HKIAAAA beacons, basement works for some of T2 expansion area and excavation works for the proposed APM depot should be treated and reused on-site as backfilling materials, although required treatment level / detail and the specific re-use mode are under development.		I
10.5.1.1	7.1	-	The following good site practices should be performed during the construction activities include: - Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; - Training of site personnel in proper waste management and chemical waste handling procedures; - Provision of sufficient waste disposal points and regular collection for disposal; - Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks by tarpaulin/ similar material or by transporting wastes in enclosed containers. The cover should be extended over the edges of the sides and tailboards; - Stockpiles of C&D materials should be kept wet or covered by impervious sheets to avoid wind-blown dust; - All dusty materials including C&D materials should be sprayed with water immediately prior to any loading transfer operation so as to keep the dusty material wet during material handling at the barging points/ stockpile areas; - C&D materials to be delivered to and from the project site by barges or by trucks should be kept wet or covered to avoid wind-blown dust; - The speed of the trucks including dump trucks carrying C&D or waste materials within the site should be controlled to about 10 km/hour in order to reduce the adverse dust impact and secure the safe movement around the site; and - To avoid or minimise dust emission during transport of C&D or waste materials within the site, each and every main temporary access should be paved with concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials. Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet.	Project Site Area / Construction Phase	I
10.5.1.3	7.1	-	The following practices should be performed to achieve waste reduction include: Use of steel or aluminium formworks and falseworks for temporary works as far as practicable;	Project Site Area / Construction Phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- Adoption of repetitive design to allow reuse of formworks as far as practicable; - Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; - Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force; - Any unused chemicals or those with remaining functional capacity should be collected for reused as far as practicable; - Proper storage and site practices to minimise the potential for damage or contamination of construction materials; and - Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.		
10.5.1.5	7.1		Inert and non-inert C&D materials should be handled and stored separately to avoid mixing the two types of materials.	Project Site Area / Construction Phase	I
10.5.1.5	7.1	-	Any recyclable materials should be segregated from the non-inert C&D materials for collection by reputable licensed recyclers whereas the non-recyclable waste materials should be disposed of at the designated landfill site by a reputable licensed waste collector.	Project Site Area / Construction Phase	I
10.5.1.6	7.1	-	A trip-ticket system promulgated shall be developed in order to monitor the off-site delivery of surplus inert C&D materials that could not be reused on-site for the proposed land formation work at the PFRF and to control fly tipping.	Project Site Area / Construction Phase	I
10.5.1.6	7.1	2.32	The Contractor should prepare and implement a Waste Management Plan detailing various waste arising and waste management practices.	Construction Phase	I
10.5.1.16	7.1	-	The following mitigation measures are recommended during excavation and treatment of the sediments: - On-site remediation should be carried out in an enclosed area in order to minimise odour/dust emissions; - The loading, unloading, handling, transfer or storage of treated and untreated sediment should be carried out in such a manner to prevent or minimise dust emissions; - All practical measures, including but not limited to speed control for vehicles, should be taken to minimise dust emission; - Good housekeeping should be maintained at all times at the sediment treatment facility and storage area; - Treated and untreated sediment should be clearly separated and stored separately; and - Surface runoff from the enclosed area should be properly collected and stored separately, and then properly treated to levels in compliance with the relevant effluent standards as required by the Water Pollution Control Ordinance before final discharge.	Project Site Area / Construction Phase	I I I I I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
10.5.1.18	7.1	-	The marine sediments to be removed from the cable field joint area would be disposed of at the designated disposal sites to be allocated by the MFC. The following mitigation measures should be strictly followed to minimise potential impacts on water quality during transportation of the sediments requiring Type 1 disposal: - Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material; - Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by EPD; and - Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation.	Project Site Area / Construction Phase	N/A – the field joint excavation works for the submarine cable diversion will no longer be conducted anymore
10.5.1.19	7.1	-	Contractor should register with the EPD as a chemical waste producer and to follow the relevant guidelines. The following measures should be implemented: - Good quality containers compatible with the chemical wastes should be used; - Incompatible chemicals should be stored separately; - Appropriate labels must be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc.; and - The contractor will use a licensed collector to transport and dispose of the chemical wastes at the approved Chemical Waste Treatment Centre or other licensed recycling facilities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Project Site Area / Construction Phase	I
10.5.1.20	7.1	-	General refuse should be stored in enclosed bins or compaction units separated from inert C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site for disposal at designated landfill sites. An enclosed and covered area should be provided to reduce the occurrence of 'windblown' light material.	Project Site Area / Construction Phase	I
10.5.1.21	7.1	-	The construction contractors will be required to regularly check and clean any refuse trapped or accumulated along the newly constructed seawall. Such refuse will then be stored and disposed of together with the general refuse.	Project Site Area / Construction Phase	I
Land Contamination – Construction Phase					
11.10.1.2 to 11.10.1.3	8.1	2.32	For areas inaccessible during site reconnaissance survey Further site reconnaissance would be conducted once the areas are accessible in order to identify any land contamination concern for the areas.	Project Site Area inaccessible during site reconnaissance / Prior to Construction Phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Subject to further site reconnaissance findings, a supplementary Contamination Assessment Plan (CAP) for additional site investigation (SI) (if necessary) may be prepared and submitted to EPD for endorsement prior to the commencement of SI at these areas.		C – Completed in Jan 2018
			After completion of SI, the Contamination Assessment Report (CAR) will be prepared and submitted to EPD for approval prior to start of the proposed construction works at the golf course, the underground and above-ground fuel storage tank areas, emergency power generation units, airside petrol filling station and fuel tank room.		I *(CAR for golf course and Terminal 2 emergency power supply system nos.1, 2, 3, 4 and 5 were submitted to EPD)
			Should remediation be required, Remediation Action Plan (RAP) and Remediation Report (RR) will be prepared for EPD's approval prior to commencement of the proposed remediation and any construction works respectively.		N/A as no remediation was required.
11.8.1.2	8.1	-	If contaminated soil is identified, the following mitigation measures are for the excavation and transportation of contaminated materials (if any): - To minimize the incidents of construction workers coming in contact with any contaminated materials, bulk earth-moving excavation equipment should be employed; - Contact with contaminated materials can be minimised by wearing appropriate clothing and personal protective equipment such as gloves and masks (especially when working directly with contaminated material), provision of washing facilities and prohibition of smoking and eating on site; - Stockpiling of contaminated excavated materials on site should be avoided as far as possible; - The use of any contaminated soil for landscaping purpose should be avoided unless pre-treatment was carried out; - Vehicles containing any excavated materials should be suitably covered to reduce dust emissions and/or release of contaminated wastewater; - Truck bodies and tailgates should be sealed to prevent any discharge; - Only licensed waste haulers should be used to collect and transport contaminated material to treatment/disposal site and should be equipped with tracking system to avoid fly tipping; - Speed control for trucks carrying contaminated materials should be exercised. 8km/h is the recommended speed limit; - Strictly observe all relevant regulations in relation to waste handling, such as Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 354) and obtain all necessary permits where required; and - Maintain records of waste generation and disposal quantities and disposal arrangements.	Project Site Area / Construction Phase	N/A as no contaminated soil was found.

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
Terrestrial Ecological – Construction Phase					
12.10.1.1	9.2	2.14	Pre-construction Egretty Survey Conduct ecological survey for Sha Chau egretty to update the latest boundary of the egretty.	Breeding season (April - July) prior to commencement of HDD drilling works at HKIA	C – Completed in Jan 2019
12.7.2.3 and 12.7.2.6	9.1	2.30	Avoidance and Minimisation of Direct Impact to Egretty - The daylighting location will avoid direct encroachment to the Sheung Sha Chau egretty. The daylighting location and mooring of flat top barge, if required, will be kept away from the egretty; - In any event, controls such as demarcation of construction site boundary and confining the lighting within the site will be practised to minimise disturbance to off-site habitat at Sheung Sha Chau Island; and - The containment pit at the daylighting location shall be covered or camouflaged.	During construction phase at Sheung Sha Chau Island	C – Completed in Jan 2019
12.7.2.5	9.1	2.30	Preservation of Nesting Vegetation The proposed daylighting location and the arrangement of connecting pipeline will avoid the need of tree cutting, therefore the trees that are used by ardeids for nesting will be preserved.	During construction phase at Sheung Sha Chau Island	C – Completed in Jan 2019
12.7.2.4 and 12.7.2.6	9.1	2.30	Timing the Pipe Connection Works outside Ardeid's Breeding Season All HDD and related construction works on Sheung Sha Chau Island will be scheduled outside the ardeids' breeding season (between April and July). No night-time construction work will be allowed on Sheung Sha Chau Island during all seasons.	During construction phase at Sheung Sha Chau Island	C – Completed in Jan 2019
12.10.1.1	9.3	-	Ecological Monitoring During the HDD construction works period from August to March, ecological monitoring will be undertaken monthly at the HDD daylighting location on Sheung Sha Chau Island to identify and evaluate any impacts with appropriate actions taken as required to address and minimise any adverse impact found.	at Sheung Sha Chau Island	C – Completed in Jan 2019
Marine Ecological Impact – Pre-construction Phase					
13.11.4.1	10.2.2	-	Pre-construction phase Coral Dive Survey.	HKIAAA artificial seawall	C – Completed in Jan 2016
Marine Ecological Impact – Construction Phase					
13.11.1.3 to 13.11.1.6	-	-	Minimisation of Land Formation Area Minimise the overall size of the land formation needed for the additional facilities to minimise the overall loss of habitat for marine resources, especially the CWD population.	Land formation footprint / during detailed design phase to completion of construction	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
13.11.1.7 to 13.11.1.10	-	2.31	Use of Construction Methods with Minimal Risk/Disturbance Use of non-dredge method for the main land formation and ancillary works including the diversion of the aviation fuel pipeline to the AFRF;	During construction phase at marine works area	C – Completed in Jan 2019 for diversion of aviation fuel pipeline
			Use of Deep Cement Mixing (DCM) method instead of conventional seabed dredging for the land formation works to reduce the risk of negative impacts through the elevation of suspended solids and contaminants on CWDs, fisheries and the marine environment;		I
			Use of bored piling in short duration to form the new approach lights and marker beacons for the new runway;		C – Completed in Oct 2021 for new approach lights
			Avoid bored piling during CWD peak calving season (Mar to Jun);		N/A for marker beacons as HKIAAAA Marker Beacons would be replaced by buoys
			Prohibition of underwater percussive piling; and		I
			Use of horizontal directional drilling (HDD) method and water jetting methods for placement of submarine cables and pipelines to minimise the disturbance to the CWDs and other marine ecological resources.		C – Completed in Jan 2019 for HDD works
13.11.2.1 to 13.11.2.7	-	-	Mitigation for Indirect Disturbance due to Deterioration of Water Quality Water quality mitigation measures during construction phases include consideration of alternative construction methods, deployment of silt curtain and good site practices;	All works area during the construction phase	I
			Alternative construction methods including use of non-dredge methods for ground improvement (e.g. Deep Cement Mixing (DCM), prefabricated vertical drains (PVD), sand compaction piles, steel cells, stone columns and vertical sand drains);		I
			Use of bored piling in short duration to form the new approach lights and marker beacons for the new runway; and		C – Completed in Oct 2021 for new approach lights
			Use of horizontal directional drilling (HDD) method and water jetting methods for placement of undersea cables and pipelines to minimise the disturbance to the CWDs and other marine ecological resources.		C – Completed in Jan 2019 for HDD works
13.11.1.12	-	-	Strict Enforcement of No-Dumping Policy	All works area during the construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- A policy prohibiting dumping of wastes, chemicals, oil, trash, plastic, or any other substance that would potentially be harmful to dolphins and/or their habitat in the work area; - Mandatory educational programme of the no-dumping policy be made available to all construction site personnel for all project-related works; - Fines for infractions should be implemented; and - Unscheduled, on-site audits shall be implemented.		
13.11.1.13	-	-	Good Construction Site Practices - Regular inspection of the integrity and effectiveness of all silt curtains and monitoring of effluents to ensure that any discharge meets effluent discharge guidelines; - Keep the number of working or stationary vessels present on-site to the minimum anytime; and - Unscheduled, on-site audits for all good site practice restrictions should be conducted, and fines or penalties sufficient to be an effective deterrent need to be levied against violators.	All works area during the construction phase	I
13.11.1.3 to 13.11.1.6	-	-	Minimisation of Land Formation Area Minimise the overall size of the land formation needed for the additional facilities to minimise the overall loss of habitat for marine resources, especially the CWD population.	Land formation footprint / during detailed design phase to completion of construction	I
13.11.5.4 to 13.11.5.13	10.3.1	-	SkyPier High Speed Ferries' Speed Restrictions and Route Diversions - SkyPier HSFs operating to / from Zhuhai and Macau would divert north of SCLKC Marine Park with a 15 knot speed limit to apply for the part-journeys that cross high CWD abundance grid squares as indicatively shown in Drawing No. MCL/P132/EIA/13-023 of the EIA Report. Both the alignment of the northerly route and the portion of routings to be subject to the speed limit of 15 knots shall be finalised prior to commencement of construction based on the future review of up-to-date CWD abundance and EM&A data and taking reference to changes in total SkyPier HSF numbers; and - A maximum of 10 knots will be enforced through the designated SCLKC Marine Park area at all times.	Area between the footprint and SCLKC Marine Park during construction phase	I
			Other mitigation measures - The ET will audit various parameters including actual daily numbers of HSFs, compliance with the 15-knot speed limit in the speed control zone and diversion compliance for SkyPier HSFs operating to / from Zhuhai and Macau; and - The effectiveness of the CWD mitigation measures after implementation of initial six month SkyPier HSF diversion and speed restriction will be reviewed.	Area between the footprint and SCLKC Marine Park during construction phase	I C – Completed in Sep 2016
13.11.5.14 to 13.11.5.18	10.3.1	2.31	Dolphin Exclusion Zone Establishment of a 24 hr Dolphin Exclusion Zone (DEZ) with a 250 m radius around the land formation works areas;	Marine waters around land formation works area during construction phase	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			- A DEZ would also be implemented during ground improvement works (e.g. DCM), water jetting works for submarine cables diversion, open trench dredging at the field joint locations and seawall construction; and - A DEZ would also be implemented during bored piling work but as a precautionary measure only.		I C – Completed in Oct 2021 for the bored piling work of New approach lights
13.11.5.19	10.4	2.31	Acoustic Decoupling of Construction Equipment - Air compressors and other noisy equipment that must be mounted on steel barges should be acoustically-decoupled to the greatest extent feasible, for instance by using rubber or air-filled tyres; and - Specific acoustic decoupling measures shall be specified during the detailed design of the project for use during the land formation works.	Around coastal works area during construction phase	I
13.11.5.20	10.6.1	2.29	Spill Response Plan An oil and hazardous chemical spill response plan is proposed to be established during the construction phase as a precautionary measure so that appropriate actions to prevent or reduce risks to CWDs can be undertaken in the event of an accidental spillage.	Construction phase	I
13.11.5.21 to 13.11.5.23	10.6.1	-	Construction Vessel Speed Limits and Skipper Training - A speed limit of 10 knots should be strictly observed for construction vessels at areas with the highest CWD densities (as currently indicated by the 1x1km grid squares in Figure 6 of Appendix 13.2 of EIA report). - Vessels traversing through the work areas should be required to use predefined and regular routes (which would presumably become known to resident dolphins) to reduce disturbance to cetaceans due to vessel movements. Specific marine routes shall be specified by the Contractor prior to construction commencing.	All areas north and west of Lantau Island during construction phase	I
Fisheries Impact – Construction Phase					
14.9.1.2 to 14.9.1.5	-		Minimisation of Land Formation Area Minimise the overall size of the land formation needed for the additional facilities to minimise the overall loss of habitat for fisheries resources.	Land formation footprint / during detailed design phase to completion of construction	I
14.9.1.6	-	-	Use of Construction Methods with Minimal Risk/Disturbance Use of non-dredge method for the main land formation and ancillary works including the diversion of the aviation fuel pipeline to the AFRF;	During construction phase at marine works area	C – Completed in Jan 2019 for diversion of aviation fuel pipeline

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Use of Deep Cement Mixing (DCM) method instead of conventional seabed dredging for the land formation works to reduce the risk of negative impacts through the elevation of suspended solids and contaminants on fisheries and the marine environment;		I
			Use of bored piling in short duration to form the new approach lights and marker beacons for the new runway; and		C – Completed in Oct 2021 for new approach lights N/A for marker beacons as HKIAAAA Marker Beacons would be replaced by buoys
			Use of horizontal directional drilling (HDD) method and water jetting methods for placement of undersea cables and pipelines to minimise the disturbance to fisheries resources.		C – Completed in Jan 2019 for HDD works
14.9.1.11	-		Strict Enforcement of No-Dumping Policy - A policy prohibiting dumping of wastes, chemicals, oil, trash, plastic, or any other substance that would potentially be harmful to dolphins and/or their habitat in the work area; - Mandatory educational programme of the no-dumping policy be made available to all construction site personnel for all project-related works; - Fines for infractions should be implemented; and - Unscheduled, on-site audits shall be implemented.	All works area during the construction phase	I
14.9.1.12	-		Good Construction Site Practices - Regular inspection of the integrity and effectiveness of all silt curtains and monitoring of effluents to ensure that any discharge meets effluent discharge guidelines; - Keep the number of working or stationary vessels present on-site to the minimum anytime; and - Unscheduled, on-site audits for all good site practice restrictions should be conducted, and fines or penalties sufficient to be an effective deterrent need to be levied against violators.	All works area during the construction phase	I
14.9.1.13 to 14.9.1.18	-		Mitigation for Indirect Disturbance due to Deterioration of Water Quality - Water quality mitigation measures during construction phases include consideration of alternative construction methods, deployment of silt curtain and good site practices; - Alternative construction methods including use of non-dredge methods for ground improvement (e.g. Deep Cement Mixing (DCM), prefabricated vertical drains (PVD), sand compaction piles, steel cells, stone columns and vertical sand drains);	All works area during the construction phase	I
					I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
			Use of bored piling in short duration to form the new approach lights and marker beacons for the new runway; and		C – Completed in Oct 2021 for new approach lights N/A for marker beacons as HKIAAAA Marker Beacons would be replaced by buoys
			Use of horizontal directional drilling (HDD) method and water jetting methods for placement of undersea cables and pipelines to minimise the disturbance to fisheries resources.		C – Completed on Jan 2019 for HDD work
Landscape and Visual Impact – Construction Phase					
Table 15.6	12.3	-	CM1 - The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape.	All works areas for duration of works; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM2 - Reduction of construction period to practical minimum.	All works areas for duration of works; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM3 - Phasing of the construction stage to reduce visual impacts during the construction phase.	All works areas for duration of works; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM4 - Construction traffic (land and sea) including construction plants, construction vessels and barges should be kept to a practical minimum.	All works areas for duration of works; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM5 - Erection of decorative mesh screens or construction hoardings around works areas in visually unobtrusive colours.	All works areas for duration of works; Upon handover and completion of works. – may be disassembled in phases.	I

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
Table 15.6	12.3	-	CM6 - Avoidance of excessive height and bulk of site buildings and structures.	New passenger concourse, terminal 2 expansion and other proposed airport related buildings and structures under the project; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM7 - Control of night-time lighting by hooding all lights and through minimisation of night working periods.	All works areas for duration of works; Upon handover and completion of works. – may be disassembled in phases.	I
Table 15.6	12.3	-	CM8 - All existing trees shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas.	All existing trees to be retained; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM9 - Trees unavoidably affected by the works shall be transplanted where practical. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.	All existing trees to be affected by the works; Upon handover and completion of works.	I
Table 15.6	12.3	-	CM10 - Land formation works shall be followed with advanced hydroseeding around taxiways and runways as soon as practical.	All affected existing grass areas around runways and verges/Duration of works; Upon handover and completion of works.	I
Cultural Heritage Impact – Construction Phase					
Not applicable to the construction stage of this project.					
Health Impact – Aircraft Emissions					
Not applicable to the construction stage of this project.					

EIA Ref.	EM&A Ref.	EP Condition	Environmental Protection Measures	Location / Duration of measures Timing of completion of measures	Mitigation Measures Implemented?^
Health Impact – Aircraft Noise					
Not applicable to the construction stage of this project.					

Notes:

“ - ” For items denoted as “ - ” provided under the columns of EM&A Ref. or EP Condition, environmental protection measures should be referred to the relevant paragraph(s) / table(s) in the approved EIA Report.

“ I ” Implemented and on-going where applicable.

“ N/A ” Not applicable to the construction works implemented during the reporting month.

“ ^ ” Checked by ET through site inspection and record provided by the Contractor.

Appendix B. Monitoring Schedule

Monitoring Schedule of This Reporting Period

Feb-22

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4 Site Inspection NM4, NM6 WQ General & Regular DCM mid-ebb: 15:36 mid-flood: 10:06	5 AR1A, AR2
6 WQ General & Regular DCM mid-ebb: 16:59 mid-flood: 11:04	7 Site Inspection CWD Survey (Vessel)	8 Site Inspection CWD Survey (Vessel) WQ General & Regular DCM mid-ebb: 05:11 mid-flood: 11:49	9 CWD Survey (Vessel) NM4, NM6	10 Site Inspection CWD Survey (Vessel) WQ General & Regular DCM mid-ebb: 21:21 mid-flood: 08:32	11 Site Inspection CWD Survey (Land-based) AR1A, AR2 NM1A, NM5	12 WQ General & Regular DCM mid-ebb: 23:08 mid-flood: 10:48
13	14 Site Inspection CWD Survey (Vessel)	15 Site Inspection CWD Survey (Vessel) WQ General & Regular DCM mid-ebb: 12:41 mid-flood: 07:36	16 CWD Survey (Land-based) NM4, NM6	17 Site Inspection AR1A, AR2 NM1A, NM5 WQ General & Regular DCM mid-ebb: 13:45 mid-flood: 08:26	18 ^[1] Site Inspection	19 WQ General & Regular DCM mid-ebb: 14:49 mid-flood: 09:13
20	21 Site Inspection	22 Site Inspection NM4, NM6 WQ General & Regular DCM mid-ebb: 16:50 mid-flood: 10:33	23 AR1A, AR2 NM1A, NM5	24 Site Inspection WQ General & Regular DCM mid-ebb: 06:11 mid-flood: 11:47	25 Site Inspection	26 WQ General & Regular DCM mid-ebb: 21:55 mid-flood: 09:14
27	28 Site Inspection	1 Site Inspection AR1A, AR2 NM1A, NM5 WQ General & Regular DCM mid-ebb: 13:20 mid-flood: 07:50	2 CWD Survey (Vessel) NM4, NM6	3 Site Inspection WQ General & Regular DCM mid-ebb: 14:30 mid-flood: 08:48	4 Site Inspection CWD Survey (Vessel)	5 WQ General & Regular DCM mid-ebb: 15:29 mid-flood: 09:25
		Notes: CWD - Chinese White Dolphin Air quality and Noise Monitoring Station WQ - Water Quality DCM - Deep Cement Mixing [1] The vessel operators' son was tested positive with Rapid Antigen Test on 18 February 2022. In view of health and safety of the monitoring team, two days of CWD vessel survey scheduled after 18 February 2022 were suspended and re-scheduled to 2 and 4 March 2022 for supplementary survey. NM1A/AR1A - Man Tung Road Park NM4 - Ching Chung Hau Po Woon Primary School NM5/AR2 - Village House, Tin Sum NM6 - House No. 1, Sha Lo Wan				

Tentative Monitoring Schedule of Next Reporting Period

Mar-22

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1 Site Inspection AR1A, AR2 NM1A, NM5 WQ General & Regular DCM mid-ebb: 12:42 mid-flood: 07:17	2 CWD Survey (Vessel) NM4, NM6	3 Site Inspection WQ General & Regular DCM mid-ebb: 13:56 mid-flood: 08:21	4 Site Inspection CWD Survey (Vessel)	5
6 WQ General & Regular DCM mid-ebb: 15:29 mid-flood: 09:25	7 Site Inspection CWD Survey (Vessel) AR1A, AR2 NM1A, NM5	8 Site Inspection CWD Survey (Vessel) NM4, NM6 WQ General & Regular DCM mid-ebb: 16:41 mid-flood: 10:02	9	10 Site Inspection CWD Survey (Vessel) WQ General & Regular DCM mid-ebb: 18:35 mid-flood: 10:36	11 Site Inspection CWD Survey (Vessel)	12 AR1A, AR2 WQ General & Regular DCM mid-ebb: 21:20 mid-flood: 08:46
13	14 Site Inspection CWD Survey (Vessel)	15 Site Inspection CWD Survey (Vessel) WQ General & Regular DCM mid-ebb: 11:53 mid-flood: 16:58	16	17 Site Inspection CWD Survey (Vessel) NM4, NM6 WQ General & Regular DCM mid-ebb: 12:50 mid-flood: 07:17	18 Site Inspection CWD Survey (Vessel) AR1A, AR2 NM1A, NM5	19 WQ General & Regular DCM mid-ebb: 13:50 mid-flood: 08:01
20	21 Site Inspection	22 Site Inspection WQ General & Regular DCM mid-ebb: 15:40 mid-flood: 09:17	23 NM4, NM6	24 Site Inspection AR1A, AR2 NM1A, NM5 WQ General & Regular DCM mid-ebb: 17:27 mid-flood: 10:20	25 Site Inspection	26 WQ General & Regular DCM mid-ebb: 20:12 mid-flood: 07:20
27	28 Site Inspection CWD Survey (Land-based)	29 Site Inspection CWD Survey (Land-based) NM4, NM6 WQ General & Regular DCM mid-ebb: 11:50 mid-flood: 16:54	30 AR1A, AR2 NM1A, NM5	31 Site Inspection WQ General & Regular DCM mid-ebb: 12:59 mid-flood: 07:10		
		Notes: CWD - Chinese White Dolphin Air quality and Noise Monitoring Station WQ - Water Quality DCM - Deep Cement Mixing NM1A/AR1A - Man Tung Road Park NM4 - Ching Chung Hau Po Woon Primary School NM5/AR2 - Village House, Tin Sum NM6 - House No. 1, Sha Lo Wan				

Appendix C. Monitoring Results

Air Quality Monitoring Results

1-hour TSP Results



Station: AR1A- Man Tung Road Park

Date	Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hr TSP ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
05-Feb-22	12:41	Fine	4.2	329	34	306	500
05-Feb-22	13:41	Fine	4.4	339	35	306	500
05-Feb-22	14:41	Fine	5.8	323	37	306	500
11-Feb-22	8:55	Sunny	6.4	80	33	306	500
11-Feb-22	9:55	Sunny	4.4	68	36	306	500
11-Feb-22	10:55	Sunny	4.7	336	72	306	500
17-Feb-22	12:15	Drizzle	8.9	88	124	306	500
17-Feb-22	13:15	Drizzle	9.4	89	85	306	500
17-Feb-22	14:15	Drizzle	9.2	74	74	306	500
23-Feb-22	12:35	Overcast	5.0	336	21	306	500
23-Feb-22	13:35	Overcast	5.0	352	33	306	500
23-Feb-22	14:35	Overcast	4.2	352	26	306	500

1-hour TSP Results

Station: AR2- Village House, Tin Sum

Date	Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hr TSP ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
05-Feb-22	8:18	Fine	2.8	41	28	298	500
05-Feb-22	9:18	Fine	3.6	42	29	298	500
05-Feb-22	10:18	Fine	2.2	349	29	298	500
11-Feb-22	13:36	Sunny	2.5	307	75	298	500
11-Feb-22	14:36	Sunny	2.8	301	62	298	500
11-Feb-22	15:36	Sunny	2.5	263	60	298	500
17-Feb-22	8:30	Drizzle	7.2	92	97	298	500
17-Feb-22	9:30	Drizzle	5.8	84	105	298	500
17-Feb-22	10:30	Drizzle	10.8	104	103	298	500
23-Feb-22	8:36	Overcast	2.5	37	25	298	500
23-Feb-22	9:36	Overcast	3.3	6	19	298	500
23-Feb-22	10:36	Overcast	3.3	352	27	298	500

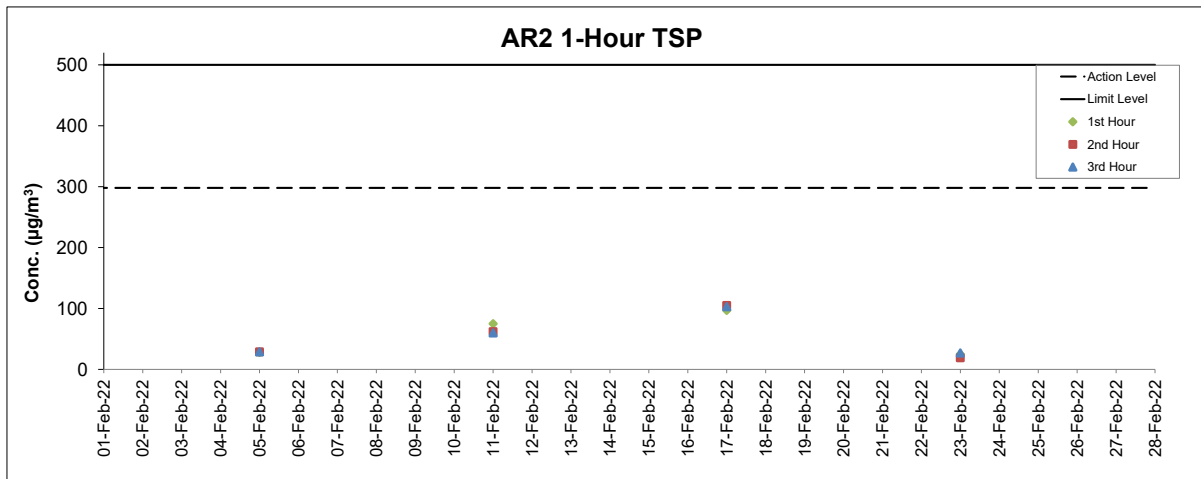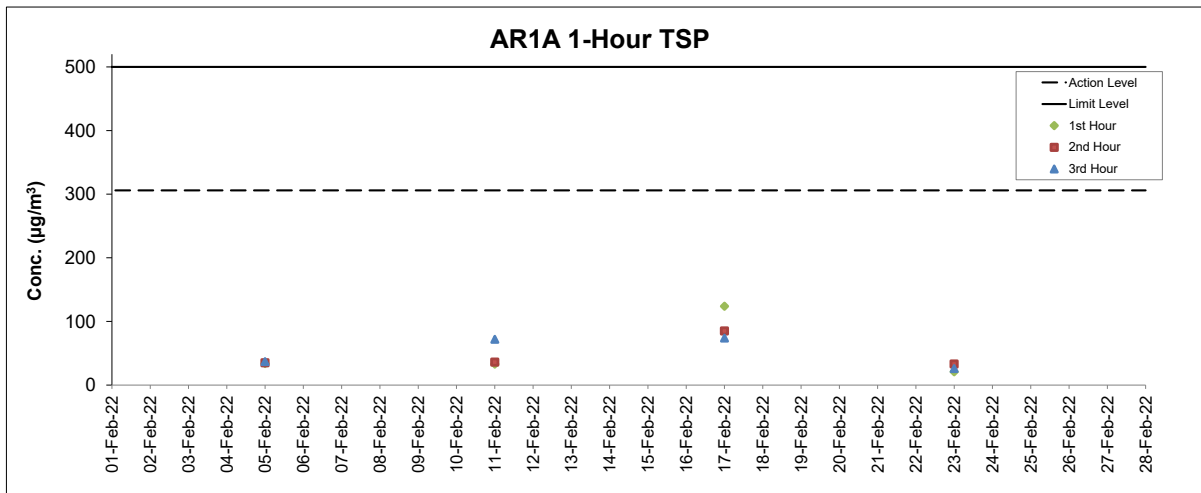

Notes

- Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.
- Weather conditions during monitoring are presented in the data tables above.
- QA/QC requirements as stipulated in the EM&A Manual were carried out during measurement.

Noise Monitoring Results

Noise Measurement Results

Station: NM1A- Man Tung Road Park

Date	Weather	Time	Measured L ₁₀ dB(A)	Measured L ₅₀ dB(A)	L _{eq(30mins)} dB(A) ^
11-Feb-22	Sunny	11:11	55.8	50.1	57
11-Feb-22	Sunny	11:16	56.2	50.3	
11-Feb-22	Sunny	11:21	58.2	50.6	
11-Feb-22	Sunny	11:26	56.9	50.4	
11-Feb-22	Sunny	11:31	55.6	48.9	
11-Feb-22	Sunny	11:36	55.8	49.4	
17-Feb-22	Drizzle	12:16	63.7	53.1	61
17-Feb-22	Drizzle	12:21	59.6	52.3	
17-Feb-22	Drizzle	12:26	59.9	53.3	
17-Feb-22	Drizzle	12:31	61.4	53.0	
17-Feb-22	Drizzle	12:36	58.0	52.1	
17-Feb-22	Drizzle	12:41	58.8	52.0	
23-Feb-22	Overcast	12:28	55.6	50.6	58
23-Feb-22	Overcast	12:33	58.3	51.8	
23-Feb-22	Overcast	12:38	56.6	50.1	
23-Feb-22	Overcast	12:43	59.2	51.1	
23-Feb-22	Overcast	12:48	60.2	51.4	
23-Feb-22	Overcast	12:53	58.4	52.1	

Remarks:

(^)+3dB (A) correction in Leq(30mins) dB(A) was applied to free-field measurement.

Noise Measurement Results

Station: NM4- Ching Chung Hau Po Woon Primary School

Date	Weather	Time	Measured L ₁₀ dB(A)	Measured L ₅₀ dB(A)	L _{eq(30mins)} dB(A) ^
04-Feb-22	Sunny	13:47	58.7	53.3	60
04-Feb-22	Sunny	13:52	58.5	53.8	
04-Feb-22	Sunny	13:57	58.3	53.5	
04-Feb-22	Sunny	14:02	58.9	53.8	
04-Feb-22	Sunny	14:07	58.9	53.5	
04-Feb-22	Sunny	14:12	60.1	53.5	
09-Feb-22	Overcast	13:40	58.7	53.6	60
09-Feb-22	Overcast	13:45	58.8	52.9	
09-Feb-22	Overcast	13:50	59.3	52.8	
09-Feb-22	Overcast	13:55	60.3	54.1	
09-Feb-22	Overcast	14:00	59.2	54.0	
09-Feb-22	Overcast	14:05	58.6	54.2	
16-Feb-22	Fine	13:29	59.7	54.5	62
16-Feb-22	Fine	13:34	60.8	56.1	
16-Feb-22	Fine	13:39	60.4	56.2	
16-Feb-22	Fine	13:44	59.6	56.4	
16-Feb-22	Fine	13:49	61.1	57.2	
16-Feb-22	Fine	13:54	62.5	57.3	
22-Feb-22	Overcast	08:38	60.8	55.1	62
22-Feb-22	Overcast	08:43	62.6	55.8	
22-Feb-22	Overcast	08:48	61.1	56.1	
22-Feb-22	Overcast	08:53	60.6	56.4	
22-Feb-22	Overcast	08:58	62.0	55.2	
22-Feb-22	Overcast	09:03	60.7	53.1	

Remarks:

(^)+3dB (A) correction in Leq(30mins) dB(A) was applied to free-field measurement.

Noise Measurement Results

Station: NM5- Village House, Tin Sum

Date	Weather	Time	Measured L ₁₀ dB(A)	Measured L ₉₀ dB(A)	L _{eq(30mins)} dB(A) ^
11-Feb-22	Sunny	14:41	60.6	45.9	53*
11-Feb-22	Sunny	14:46	53.2	46.5	
11-Feb-22	Sunny	14:51	50.2	45.2	
11-Feb-22	Sunny	14:56	50.3	44.5	
11-Feb-22	Sunny	15:01	48.6	44.6	
11-Feb-22	Sunny	15:06	51.1	45.6	
17-Feb-22	Drizzle	08:34	61.0	53.3	58
17-Feb-22	Drizzle	08:39	54.9	49.5	
17-Feb-22	Drizzle	08:44	57.4	50.3	
17-Feb-22	Drizzle	08:49	54.0	49.8	
17-Feb-22	Drizzle	08:54	54.9	51.6	
17-Feb-22	Drizzle	08:59	53.8	50.8	
23-Feb-22	Overcast	09:48	54.0	48.6	56
23-Feb-22	Overcast	09:53	55.8	48.9	
23-Feb-22	Overcast	09:58	53.1	49.2	
23-Feb-22	Overcast	10:03	51.7	49.5	
23-Feb-22	Overcast	10:08	53.2	49.8	
23-Feb-22	Overcast	10:13	59.2	49.3	

Remarks:

(^) +3dB (A) correction in Leq(30mins) dB(A) was applied to free-field measurement.

(*) The measurement result was corrected with reference to the baseline monitoring levels.

Noise Measurement Results





Station: NM6- House No.1 Sha Lo Wan

Date	Weather	Time	Measured L ₁₀ dB(A)	Measured L ₉₀ dB(A)	L _{eq(30mins)} dB(A) ^
04-Feb-22	Sunny	15:37	60.1	44.5	64
04-Feb-22	Sunny	15:42	58.5	45.2	
04-Feb-22	Sunny	15:47	49.6	45.8	
04-Feb-22	Sunny	15:52	57.4	46.6	
04-Feb-22	Sunny	15:57	68.2	50.2	
04-Feb-22	Sunny	16:02	59.3	46.6	
09-Feb-22	Overcast	15:40	59.2	50.3	67
09-Feb-22	Overcast	15:45	70.0	51.4	
09-Feb-22	Overcast	15:50	62.3	48.9	
09-Feb-22	Overcast	15:55	54.3	49.9	
09-Feb-22	Overcast	16:00	54.4	49.4	
09-Feb-22	Overcast	16:05	52.4	48.2	
16-Feb-22	Fine	15:38	64.9	48.9	62
16-Feb-22	Fine	15:43	64.1	50.6	
16-Feb-22	Fine	15:48	60.7	51.1	
16-Feb-22	Fine	15:53	59.0	42.7	
16-Feb-22	Fine	15:58	48.1	41.8	
16-Feb-22	Fine	16:03	63.5	46.0	
22-Feb-22	Overcast	09:40	72.0	57.4	68*
22-Feb-22	Overcast	09:45	70.5	53.4	
22-Feb-22	Overcast	09:50	57.7	51.3	
22-Feb-22	Overcast	09:55	69.0	54.9	
22-Feb-22	Overcast	10:00	71.0	53.9	
22-Feb-22	Overcast	10:05	67.4	51.9	

Remarks:

(^) +3dB (A) correction in Leq(30mins) dB(A) was applied to free-field measurement.

(*) The measurement result was corrected with reference to the baseline monitoring levels.

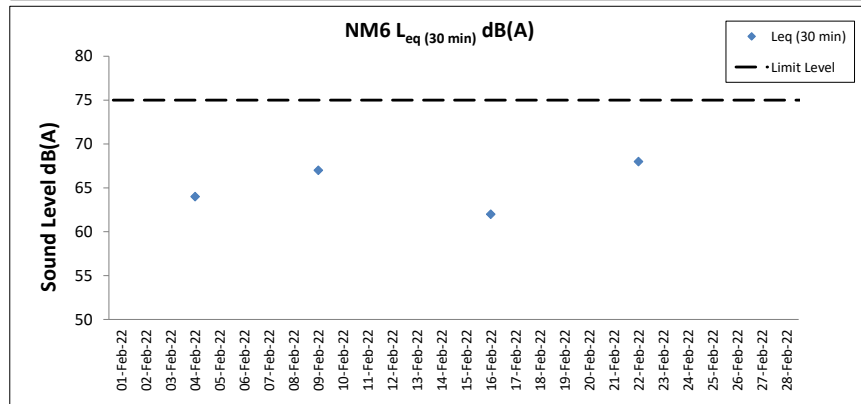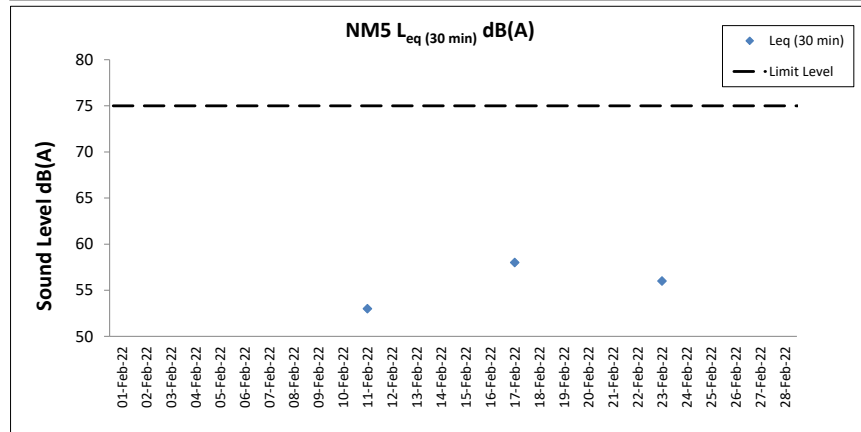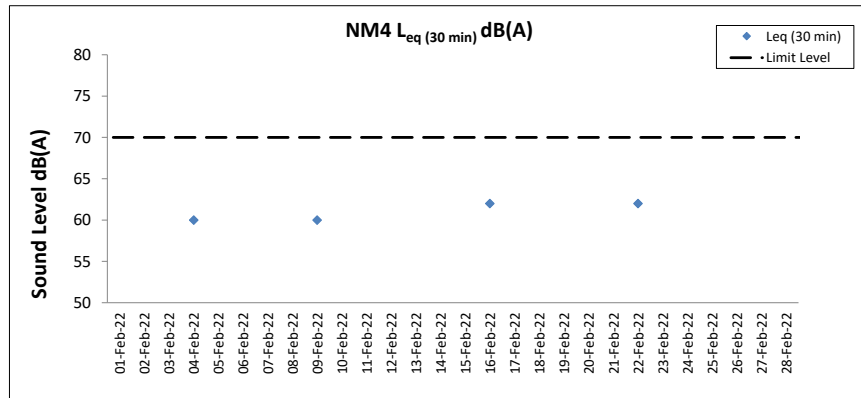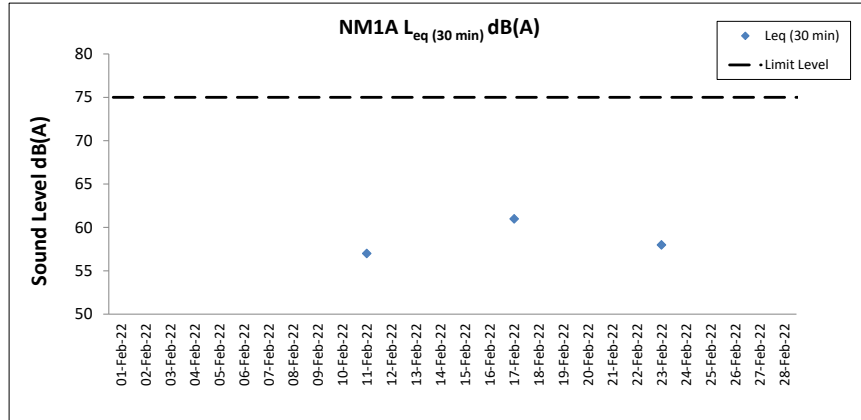

Notes

1. Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.
2. Weather conditions during monitoring are presented in the data tables above.
3. QA/QC requirements as stipulated in the EM&A Manual were carried out during measurement.

Water Quality Monitoring Results

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 04 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Cloudy	Moderate	14:57	8.5	Surface	1.0	0.2	202	16.3	16.3	8.1	8.1	31.6	31.6	100.3	100.2	8.2	8.0	8.8	9.5	5	8	47	49	815598	804261	<0.2	<0.2	0.8	0.7
						1.0	0.2	197	16.2	8.1	8.1	31.6	100.1	8.2	8.7	4	46		<0.2		0.7									
					Middle	4.3	0.2	219	16.1	16.2	8.1	8.1	32.0	32.0	95.8	95.9	7.8	9.7	9	50	<0.2	0.7								
						4.3	0.2	222	16.2	16.2	8.1	8.1	32.0	95.9	7.8	9.6	9	48	<0.2	0.8										
					Bottom	7.5	0.2	204	16.4	16.4	8.1	8.1	31.7	31.7	97.2	97.3	7.9	10.1	9	52	<0.2	0.6								
						7.5	0.3	199	16.4		8.1	31.6	97.4		7.9		10.2	9	52	<0.2	0.7									
C2	Cloudy	Moderate	13:51	11.9	Surface	1.0	0.0	6	16.7	16.7	8.0	8.0	29.3	29.3	100.4	100.4	8.2	8.0	3.7	4.4	9	8	47	50	825660	806937	<0.2	<0.2	0.7	0.7
						1.0	0.0	3	16.7	8.0	8.0	29.3	100.3	8.2	3.7	10	47		<0.2		0.7									
					Middle	6.0	0.1	17	16.6	16.6	8.0	8.0	31.6	31.5	95.6	95.7	7.7	4.2	7	49	<0.2	0.6								
						6.0	0.1	11	16.6	8.0	31.5	95.7	7.7	4.2	8	50	<0.2	0.7												
					Bottom	10.9	0.0	0	16.7	16.7	8.0	8.0	31.4	31.3	97.3	97.6	7.9	5.4	8	52	<0.2	0.8								
						10.9	0.0	358	16.7	8.0	31.3	97.8	7.9	5.4	7	53	<0.2	0.7												
C3	Cloudy	Moderate	15:03	11.8	Surface	1.0	0.3	98	16.7	16.7	8.0	8.0	32.8	32.8	102.2	102.2	8.1	8.0	4.3	6.2	10	9	47	49	822127	817812	<0.2	<0.2	0.7	0.7
						1.0	0.3	92	16.7	8.0	8.0	32.8	102.2	8.1	4.3	9	47		<0.2		0.6									
					Middle	5.9	0.4	70	16.6	16.6	8.0	8.0	33.2	33.2	97.4	97.4	7.8	6.0	10	48	<0.2	0.7								
						5.9	0.3	77	16.6	8.0	33.2	97.4	7.8	6.2	9	49	<0.2	0.7												
					Bottom	10.8	0.3	90	16.5	16.5	8.0	8.0	33.2	33.2	98.0	98.0	7.8	8.0	9	51	<0.2	0.6								
						10.8	0.3	85	16.5	8.0	33.2	98.1	7.8	8.3	9	52	<0.2	0.7												
IM1	Cloudy	Moderate	14:38	6.9	Surface	1.0	0.0	168	16.5	16.5	8.1	8.1	31.5	31.5	98.5	98.5	8.0	8.0	7.0	7.8	4	3	47	48	818337	806452	<0.2	<0.2	0.7	0.7
						1.0	0.1	163	16.5	8.1	8.1	31.6	98.4	8.0	7.1	3	46		<0.2		0.7									
					Middle	3.5	0.1	179	16.3	16.3	8.1	8.1	31.7	31.7	97.6	97.6	7.9	7.7	3	49	<0.2	0.7								
						3.5	0.1	179	16.3	8.1	31.7	97.5	7.9	7.8	2	48	<0.2	0.6												
					Bottom	5.9	0.1	195	16.5	16.5	8.0	8.0	31.5	31.5	96.8	96.8	7.8	8.7	2	50	<0.2	0.6								
						5.9	0.1	194	16.5	8.0	31.5	96.7	7.8	8.7	2	50	<0.2	0.6												
IM2	Cloudy	Moderate	14:33	6.8	Surface	1.0	0.1	76	16.4	16.4	8.1	8.1	31.5	31.5	98.6	98.5	8.0	8.0	8.0	9.0	5	4	48	49	819181	806256	<0.2	<0.2	0.6	0.7
						1.0	0.1	81	16.4	8.1	8.1	31.5	98.4	8.0	8.0	4	46		<0.2		0.8									
					Middle	3.4	0.1	62	16.3	16.3	8.1	8.1	31.6	31.6	97.7	97.8	7.9	9.1	4	50	<0.2	0.9								
						3.4	0.1	60	16.3	8.1	31.6	97.9	8.0	9.3	4	49	<0.2	0.8												
					Bottom	5.8	0.1	60	16.6	16.7	8.1	8.1	31.4	31.4	99.6	99.7	8.1	9.9	4	51	<0.2	0.7								
						5.8	0.2	62	16.7	8.1	31.4	99.8	8.1	9.8	3	52	<0.2	0.6												
IM7	Cloudy	Moderate	14:15	8.5	Surface	1.0	0.2	66	16.6	16.6	8.1	8.1	30.7	30.7	102.1	102.1	8.3	8.3	4.3	4.9	4	3	46	49	821366	806846	<0.2	<0.2	0.6	0.6
						1.0	0.2	65	16.6	8.1	8.1	30.7	102.0	8.3	4.3	3	47		<0.2		0.6									
					Middle	4.3	0.2	58	16.5	16.5	8.1	8.1	31.1	31.1	100.6	100.6	8.2	4.7	3	49	<0.2	0.7								
						4.3	0.3	58	16.5	8.1	31.2	100.5	8.2	4.6	3	47	<0.2	0.5												
					Bottom	7.5	0.2	47	16.8	16.8	8.0	8.0	31.0	31.0	99.8	99.9	8.1	5.8	2	51	<0.2	0.7								
						7.5	0.2	41	16.8	8.0	31.0	100.0	8.1	5.8	3	52	<0.2	0.7												

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 04 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grd (Northing)	Coordinate HK Grd (Easting)	Chromium (µg/L)		Nickel (µg/L)					
									Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA		
IM10	Cloudy	Moderate	13:51	7.3	Surface	1.0	0.1	64	16.7	16.7	8.1	8.1	31.8	31.8	99.2	99.1	8.0	8.0	7.7	8.2	8	8	47	48	822225	809832	<0.2	<0.2	0.6	0.7				
						1.0	0.1	58	16.7	8.1	8.1	31.8	99.1	8.0	7.7	7	47		<0.2		0.7													
					Middle	3.7	0.1	40	16.6	16.6	8.1	8.1	32.2	32.2	98.5	98.6	7.9	8.3	8	48	<0.2	0.6												
						3.7	0.2	41	16.6	8.1	8.1	32.2	98.7	7.9	8.3	8	51	<0.2	0.7															
					Bottom	6.3	0.1	73	16.6	16.6	8.1	8.1	32.2	32.2	99.3	99.4	8.0	8.0	8.5	8	48	<0.2	0.7											
						6.3	0.2	69	16.6	16.6	8.1	8.1	32.2	99.5	8.0	8.0	8.5	8	48	<0.2	0.7													
IM11	Cloudy	Moderate	13:57	8.1	Surface	1.0	0.1	69	16.8	16.8	8.0	8.0	31.5	31.5	98.3	98.2	7.9	7.3	7.9	8	5	47	49	821497	810538	<0.2	<0.2	0.8	0.7					
						1.0	0.1	65	16.8	8.0	8.0	31.6	98.1	7.9	7.4	8	48	<0.2		0.7														
					Middle	4.1	0.2	79	16.7	16.7	8.0	8.0	31.9	31.9	97.4	97.4	7.8	7.8	4	49	<0.2	0.7												
						4.1	0.2	74	16.7	8.0	8.0	32.0	97.4	7.8	7.8	3	49	<0.2	0.8															
					Bottom	7.1	0.1	58	16.7	16.7	8.0	8.0	32.1	32.1	98.9	99.1	7.9	7.9	2	51	<0.2	0.6												
						7.1	0.1	52	16.7	8.0	8.0	32.1	99.4	8.0	8.0	2	52	<0.2	0.6															
IM12	Cloudy	Moderate	14:04	8.8	Surface	1.0	0.2	82	16.9	16.9	8.0	8.0	31.5	31.5	98.3	98.2	7.9	4.5	7.9	3	2	47	50	821184	811507	<0.2	<0.2	0.8	0.7					
						1.0	0.2	88	16.8	8.0	8.0	31.6	98.1	7.9	4.5	2	47	<0.2		0.7														
					Middle	4.4	0.2	72	16.7	16.7	8.0	8.0	32.2	32.3	97.7	97.7	7.8	5.1	3	49	<0.2	0.6												
						4.4	0.2	72	16.7	8.0	8.0	32.3	97.8	7.8	5.2	2	50	<0.2	0.7															
					Bottom	7.8	0.1	87	16.7	16.7	8.0	8.0	32.4	32.4	98.6	98.7	7.9	8.5	2	52	<0.2	0.6												
						7.8	0.1	89	16.7	8.0	8.0	32.4	98.8	7.9	9.0	2	53	<0.2	0.6															
SR1A	Cloudy	Moderate	14:30	5.6	Surface	1.0	0.0	23	16.8	16.8	8.0	8.0	32.5	32.5	100.8	100.9	8.0	4.8	8.1	3	3	-	-	819981	812653	-	-	-	-					
						1.0	0.0	25	16.8	8.0	8.0	32.5	101.1	8.1	4.8	3	-	-		-														
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.6	0.0	42	16.8	16.8	8.0	8.0	32.5	32.5	101.6	101.7	8.1	8.1	4.8	4	-	-	-			-		-		-	-	-	-	-
						4.6	0.1	40	16.8	8.0	8.0	32.5	101.8	8.1	4.7	3	-	-	-	-	-	-	-			-		-		-	-	-	-	
SR2	Cloudy	Moderate	14:43	4.4	Surface	1.0	0.2	47	16.8	16.8	8.0	8.0	32.2	32.2	101.1	101.1	8.1	4.8	8.1	5	3	49	50	821470	814179	<0.2	<0.2	0.6	0.7					
						1.0	0.2	44	16.8	8.0	8.0	32.2	101.2	8.1	4.9	4	48	<0.2		0.7														
					Middle	-	0.2	48	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	0.2	46	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
					Bottom	3.4	0.1	80	16.8	16.8	8.0	8.0	32.2	32.2	102.1	102.1	8.2	8.2	5.4	<2	51	<0.2	0.9											
						3.4	0.2	72	16.8	8.0	8.0	32.2	102.2	8.2	5.4	<2	52	<0.2	0.7															
SR3	Cloudy	Moderate	14:08	8.7	Surface	1.0	0.1	62	16.6	16.6	8.1	8.1	30.5	30.5	98.8	98.7	8.0	4.4	8.0	<2	3	-	-	822150	807572	-	-	-	-					
						1.0	0.1	64	16.6	8.1	8.1	30.6	98.5	8.0	4.4	<2	-	-		-														
					Middle	4.4	0.1	71	16.5	16.5	8.1	8.1	31.0	31.0	98.2	98.2	8.0	5.2	2	-	-	-	-			-		-		-	-	-		
						4.4	0.0	71	16.5	8.1	8.1	31.0	98.2	8.0	5.3	3	-	-	-	-	-	-	-			-		-		-	-			
					Bottom	7.7	0.1	84	16.7	16.8	8.0	8.0	30.9	30.9	98.3	98.3	8.0	6.3	3	-	-	-	-			-		-		-	-	-	-	
						7.7	0.2	79	16.8	8.0	8.0	30.8	98.3	8.0	6.3	4	-	-	-	-	-	-	-			-		-		-	-	-		
SR4A	Cloudy	Moderate	15:17	8.9	Surface	1.0	0.0	84	16.3	16.3	8.1	8.1	31.5	31.5	99.4	99.4	8.1	5.7	8.1	4	4	-	-	817202	807804	-	-	-	-					
						1.0	0.0	80	16.3	8.1	8.1	31.5	99.4	8.1	5.8	3	-	-		-		-												
					Middle	4.5	0.0	71	16.3	16.3	8.1	8.1	31.6	31.6	100.0	100.1	8.1	7.5	4	-	-	-	-			-		-		-	-	-		
						4.5	0.1	66	16.3	8.1	8.1	31.6	100.2	8.1	7.5	5	-	-	-	-	-	-	-			-		-		-	-			
					Bottom	7.9	0.0	64	16.4	16.4	8.1	8.1	31.6	31.6	100.4	100.5	8.1	7.9	4	-	-	-	-			-		-		-	-	-		
						7.9	0.0	67	16.4	8.1	8.1	31.5	100.5	8.2	7.9	5	-	-	-	-	-	-	-			-		-		-	-	-		
SR8	Cloudy	Moderate	14:10	4.1	Surface	1.0	-	-	17.1	17.1	8.1	8.1	32.1	32.1	101.9	101.9	8.1	4.6	8.1	4	3	-	-	820369	811609	-	-	-	-					
						1.0	-	-	17.1	8.1	8.1	32.1	101.9	8.1	4.6	3	-	-		-														
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	3.1	-	-	16.9	16.9	8.1	8.1	32.3	32.3	102.2	102.3	8.1	4.7	2	-	-	-	-			-		-		-	-	-	-	-
						3.1	-	-	16.9	8.1	8.1	32.3	102.3	8.2	4.8	3	-	-	-	-	-	-	-			-		-		-	-	-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 04 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Cloudy	Moderate	10:05	8.5	Surface	1.0	0.4	47	17.1	17.1	8.1	8.1	31.7	31.7	94.5	94.4	7.6	7.6	5.2	5.9	10	9	46	48	815610	804270	<0.2	<0.2	0.6	0.6
						1.0	0.4	44	17.0	8.1	8.1	31.7	31.7	94.3	94.4	7.6	5.2		9		46		<0.2				0.7			
					Middle	4.3	0.4	19	17.0	17.0	8.1	8.1	32.0	32.0	94.8	95.0	7.6	5.6	9	47	<0.2	0.6								
						4.3	0.3	18	17.0	8.1	8.1	32.0	32.0	95.1	95.0	7.6	5.5	10	48	<0.2	0.7									
					Bottom	7.5	0.4	47	16.8	16.8	8.0	8.0	32.2	32.2	95.6	95.7	7.7	7.0	7	51	<0.2	0.6								
						7.5	0.5	48	16.7	8.0	8.0	32.2	32.2	95.7	95.7	7.7	7.0	6	51	<0.2	0.6									
C2	Cloudy	Moderate	11:19	11.7	Surface	1.0	0.4	347	17.5	17.5	8.0	8.0	31.4	31.4	96.0	96.0	7.6	7.6	4.3	5.4	12	10	47	48	825658	806960	<0.2	<0.2	0.7	0.7
						1.0	0.4	353	17.5	8.0	8.0	31.4	31.4	95.9	96.0	7.6	4.3		13		46		<0.2				0.7			
					Middle	5.9	0.5	338	17.6	17.7	8.0	8.0	31.4	31.4	96.2	96.3	7.6	5.3	5	48	<0.2	0.7								
						5.9	0.4	344	17.7	8.0	8.0	31.4	31.4	96.3	96.3	7.6	5.3	12	47	<0.2	0.7									
					Bottom	10.7	0.4	338	17.8	17.8	8.0	8.0	31.3	31.3	97.2	97.6	7.7	6.6	6	50	<0.2	0.7								
						10.7	0.4	339	17.8	8.0	8.0	31.3	31.3	98.0	97.6	7.8	6.6	12	51	<0.2	0.6									
C3	Cloudy	Moderate	09:53	11.2	Surface	1.0	0.4	272	17.1	17.1	8.0	8.0	31.9	31.9	94.3	94.3	7.5	7.5	7.2	7.7	7	13	48	49	822116	817815	<0.2	<0.2	0.7	0.7
						1.0	0.5	279	17.1	8.0	8.0	31.9	31.9	94.3	94.3	7.5	7.2		13		49		<0.2				0.8			
					Middle	5.6	0.5	268	17.1	17.1	8.0	8.0	31.9	31.9	94.1	94.1	7.5	7.3	13	50	<0.2	0.7								
						5.6	0.5	262	17.1	8.0	8.0	31.9	31.9	94.1	94.1	7.5	7.3	14	50	<0.2	0.6									
					Bottom	10.2	0.5	274	17.1	17.1	8.0	8.0	31.9	31.9	93.2	93.3	7.4	8.6	15	51	<0.2	0.6								
						10.2	0.5	280	17.1	8.0	8.0	32.0	31.9	93.3	93.3	7.4	8.6	14	51	<0.2	0.6									
IM1	Cloudy	Moderate	10:24	6.5	Surface	1.0	0.2	23	17.2	17.2	8.1	8.1	31.6	31.6	94.1	94.1	7.5	7.5	6.9	7.2	13	12	45	46	818354	806454	<0.2	<0.2	0.6	0.6
						1.0	0.3	16	17.2	8.1	8.1	31.6	31.6	94.0	94.1	7.5	6.9		12		46		<0.2				0.7			
					Middle	3.3	0.2	25	17.2	17.2	8.1	8.1	31.7	31.7	93.5	93.5	7.5	7.9	11	48	<0.2	0.6								
						3.3	0.3	25	17.2	8.1	8.1	31.7	31.7	93.5	93.5	7.5	7.9	12	47	<0.2	0.6									
					Bottom	5.5	0.3	354	17.1	17.1	8.1	8.1	31.8	31.8	93.4	93.3	7.5	6.7	10	51	<0.2	0.7								
						5.5	0.4	351	17.1	8.1	8.1	31.8	31.8	93.2	93.3	7.5	6.7	11	51	<0.2	0.6									
IM2	Cloudy	Moderate	10:31	7.4	Surface	1.0	0.3	25	17.3	17.3	8.1	8.1	31.4	31.4	94.1	94.1	7.5	7.5	4.8	4.8	10	11	46	46	819168	806214	<0.2	<0.2	0.6	0.7
						1.0	0.3	23	17.3	8.1	8.1	31.4	31.4	94.0	94.1	7.5	4.8		11		46		<0.2				0.6			
					Middle	3.7	0.3	357	17.3	17.3	8.1	8.1	31.5	31.5	94.1	94.2	7.5	4.0	13	49	<0.2	0.8								
						3.7	0.3	353	17.3	8.1	8.1	31.5	31.5	94.3	94.2	7.5	4.0	12	47	<0.2	0.7									
					Bottom	6.4	0.3	41	17.2	17.2	8.1	8.1	31.5	31.6	96.0	96.1	7.7	5.5	13	51	<0.2	0.6								
						6.4	0.2	46	17.2	8.1	8.1	31.6	31.6	96.2	96.1	7.7	5.5	12	50	<0.2	0.7									
IM7	Cloudy	Moderate	10:52	8.3	Surface	1.0	0.3	21	17.5	17.5	8.1	8.1	30.7	30.7	97.3	97.2	7.8	7.8	5.0	6.2	6	9	47	46	821334	806819	<0.2	<0.2	0.8	0.6
						1.0	0.3	20	17.4	8.1	8.1	30.8	30.7	97.1	97.2	7.8	5.0		6		46		<0.2				0.6			
					Middle	4.2	0.3	13	17.3	17.3	8.1	8.1	31.3	31.3	96.1	96.1	7.7	6.2	6	49	<0.2	0.6								
						4.2	0.3	11	17.3	8.1	8.1	31.3	31.3	96.1	96.1	7.7	6.2	12	48	<0.2	0.6									
					Bottom	7.3	0.3	33	17.3	17.3	8.1	8.1	31.4	31.3	96.4	96.5	7.7	7.4	11	51	<0.2	0.6								
						7.3	0.3	36	17.3	8.1	8.1	31.3	31.3	96.6	96.5	7.7	7.5	12	51	<0.2	0.6									

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 04 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)											
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA						
IM10	Cloudy	Moderate	11:11	7.2	Surface	1.0	0.3	309	17.3	17.3	8.1	8.1	30.9	30.9	100.9	100.9	8.1	8.1	8.1	8.9	13	14	45	48	822242	809842	<0.2	<0.2	0.7	0.7										
						1.0	0.3	305	17.2	17.2	8.1	8.1	31.0	31.0	100.8	100.8	8.1		8.3		14		46				<0.2		0.7											
					Middle	3.6	0.3	309	17.2	17.2	8.1	8.1	31.2	31.2	101.0	101.0	8.1		9.0		14		48				<0.2		0.6											
						3.6	0.3	304	17.2	17.2	8.1	8.1	31.2	31.2	101.0	101.0	8.1		9.0		13		48				<0.2		0.6											
					Bottom	6.2	0.3	279	17.2	17.2	8.1	8.1	31.2	31.2	102.2	102.2	8.2	9.3	14		51	<0.2	0.6																	
						6.2	0.3	273	17.2	17.2	8.1	8.1	31.2	31.2	102.2	102.2	8.2	9.3	15		51	<0.2	0.8																	
					IM11	Cloudy	Moderate	11:01	7.8	Surface	1.0	0.4	272	17.3	17.3	8.1	8.1	31.2	31.2		99.2	99.2	7.9	7.9			7.4		7.4		12	13	46	48	821498	810566	<0.2	<0.2	0.8	0.7
											1.0	0.4	273	17.3	17.2	8.1	8.1	31.2	31.2		99.2	99.2	7.9				7.5				13		46				<0.2		0.7	
Middle	3.9	0.4	286	17.2						17.2	8.1	8.1	31.5	31.5	99.5	99.5	7.9	7.2	13	48	<0.2	0.7																		
	3.9	0.4	279	17.2						17.2	8.1	8.1	31.5	31.5	99.5	99.5	7.9	7.2	12	47	<0.2	0.6																		
Bottom	6.8	0.4	302	17.2						17.2	8.1	8.1	31.3	31.3	100.0	100.1	8.0	8.0	19	50	<0.2	0.7																		
	6.8	0.3	297	17.2						17.2	8.1	8.1	31.3	31.3	100.1	100.1	8.0	7.7	18	50	<0.2	0.8																		
IM12	Cloudy	Moderate	10:52	8.7						Surface	1.0	0.4	271	17.3	17.3	8.1	8.1	30.9	30.9	100.2	100.2	8.0	8.0	7.1	7.4	14	13	47		46	821156	811497	<0.2	<0.2			0.8		0.7	
											1.0	0.4	272	17.2	17.2	8.1	8.1	30.9	30.9	100.1	100.1	8.0		7.1		13		46					<0.2				0.6			
					Middle	4.4	0.4	295	17.2	17.2	8.1	8.1	31.4	31.4	99.0	99.0	7.9	7.3	6	48	<0.2	0.7																		
						4.4	0.4	294	17.2	17.2	8.1	8.1	31.4	31.4	98.9	99.0	7.9	7.3	13	49	<0.2	0.6																		
					Bottom	7.7	0.4	297	17.2	17.2	8.1	8.1	31.5	31.5	99.1	99.2	7.9	7.9	12	52	<0.2	0.7																		
						7.7	0.4	301	17.2	17.2	8.1	8.1	31.5	31.5	99.2	99.2	7.9	7.9	13	51	<0.2	0.6																		
					SR1A	Cloudy	Moderate	10:31	5.4	Surface	1.0	0.0	218	17.3	17.3	8.1	8.1	31.4	31.4	99.2	99.2	7.9	7.9	7.7		7.8	5	5	-	-			819974		812654	-	-	-		-
											1.0	0.1	216	17.3	17.3	8.1	8.1	31.4	31.4	99.2	99.2	7.9		7.7			5		-							-		-		
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-																		
	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-																		
Bottom	4.4	0.1	184	17.2						17.2	8.0	8.0	31.4	31.4	100.8	100.9	8.0	8.1	7.9	4	-	-	-																	
	4.4	0.1	182	17.2						17.2	8.0	8.0	31.4	31.4	101.0	101.0	8.1	7.8	5	-	-	-																		
SR2	Cloudy	Moderate	10:16	4.5						Surface	1.0	0.1	273	17.3	17.3	8.1	8.1	31.5	31.5	99.2	99.2	7.9	7.9	7.3	7.2		6	5	47	49	821481	814159		<0.2		<0.2		0.7	0.7	
											1.0	0.1	275	17.3	17.3	8.1	8.1	31.5	31.5	99.2	99.2	7.9		7.3			5		49					<0.2				0.7		
					Middle	-	0.1	250	-	-	-	-	-	-	-	-	-	-	-	-	-	-																		
						-	0.1	247	-	-	-	-	-	-	-	-	-	-	-	-	-	-																		
					Bottom	3.5	0.1	275	17.2	17.2	8.1	8.1	31.5	31.5	100.4	100.6	8.0	8.0	7.1	4	50	<0.2	0.7																	
						3.5	0.1	277	17.2	17.2	8.1	8.1	31.5	31.5	100.7	100.7	8.0	7.1	4	51	<0.2	0.8																		
					SR3	Cloudy	Moderate	11:00	8.7	Surface	1.0	0.4	348	17.5	17.5	8.1	8.1	30.3	30.3	98.5	98.4	7.9	7.9	5.6		6.3	5	5	-	-			822169	807561	-		-	-		-
											1.0	0.3	347	17.5	17.4	8.1	8.1	30.4	30.9	98.3	97.7	7.9		5.7			6		-						-			-		
Middle	4.4	0.3	334	17.4						17.4	8.1	8.1	30.9	30.9	97.7	97.7	7.8	6.1	6	-	-	-																		
	4.4	0.4	335	17.4						17.4	8.1	8.1	31.0	31.0	97.7	97.7	7.8	6.1	5	-	-	-																		
Bottom	7.7	0.4	346	17.5						17.5	8.0	8.0	31.0	31.0	98.5	98.5	7.9	7.1	5	-	-	-																		
	7.7	0.4	345	17.6						17.6	8.0	8.0	31.0	31.0	98.6	98.6	7.9	7.1	4	-	-	-																		
SR4A	Cloudy	Moderate	09:46	9.2						Surface	1.0	0.0	204	17.2	17.2	8.0	8.0	31.6	31.6	94.2	94.2	7.5	7.5	3.2	4.1		6	8	-	-	817198	807811			-	-		-	-	
											1.0	0.1	202	17.2	17.2	8.0	8.0	31.6	31.6	94.1	94.2	7.5		3.3			14		-						-			-		
					Middle	4.6	0.0	202	17.2	17.2	8.0	8.0	31.6	31.6	94.2	94.2	7.5	3.6	6	-	-	-																		
						4.6	0.1	206	17.2	17.2	8.0	8.0	31.6	31.6	94.2	94.2	7.5	3.6	6	-	-	-																		
					Bottom	8.2	0.0	194	17.2	17.2	8.0	8.0	31.6	31.6	95.4	95.5	7.6	5.5	6	-	-	-																		
						8.2	0.0	197	17.2	17.2	8.0	8.0	31.6	31.6	95.5	95.5	7.6	5.4	7	-	-	-																		
					SR8	Cloudy	Moderate	10:45	4.1	Surface	1.0	-	-	17.3	17.3	8.1	8.1	31.4	31.4	100.1	100.1	8.0	8.0	7.2		7.7	5	7	-	-			820373	811636	-		-	-		-
											1.0	-	-	17.3	17.3	8.1	8.1	31.4	31.4	100.1	100.1	8.0		7.2			6		-						-			-		
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-																			
	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-																		
Bottom	3.1	-	-	17.3						17.3	8.2	8.2	31.3	31.3	101.2	101.3	8.1	8.1	5	-	-	-																		
	3.1	-	-	17.3						17.3	8.2	8.2	31.3	31.3	101.4	101.4	8.1	8.1	13	-	-	-																		

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 06 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)										
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA							
C1	Sunny	Rough	16:44	7.9	Surface	1.0	0.3	221	16.5	16.5	8.3	8.3	32.3	32.3	96.4	96.4	7.7	7.7	8.8	7.0	17	15	82	86	815604	804243	<0.2	<0.2	0.8	0.7									
						1.0	0.3	221	16.5	8.3	8.3	32.3	32.3	96.4	96.4	7.7	8.9		17		82		<0.2				0.7												
					Middle	4.0	0.3	218	16.5	16.5	8.3	8.3	32.5	32.5	95.7	95.7	7.7		5.4		16		86				<0.2		0.7										
						4.0	0.2	213	16.5	8.3	8.3	32.5	32.5	95.7	95.7	7.7	5.4		15		86		<0.2				0.8												
					Bottom	6.9	0.3	217	16.5	16.5	8.3	8.3	32.6	32.6	94.9	94.9	7.6	6.9	13	90	<0.2	0.7																	
						6.9	0.3	219	16.5	16.5	8.3	8.3	32.6	32.6	94.9	94.9	7.6	6.9	12	90	<0.2	0.6																	
						C2	Sunny	Rough	15:15	10.2	Surface	1.0	0.0	158	16.6	16.6	8.2	8.2	31.4	31.4	94.2	94.2	7.6	7.6			1.2	2.8	3		3	82	86	825702	806950	<0.2	<0.2	0.8	0.8
												1.0	0.0	150	16.6	16.6	8.2	8.2	31.4	31.4	94.1	94.1	7.6				1.2		2			82				<0.2		0.7	
Middle	5.1	-	160	16.6	16.6						8.2	8.2	31.6	31.6	92.5	92.5	7.5	2.6	3	87	<0.2	1.0																	
	5.1	-	160	16.6	16.6						8.2	8.2	31.6	31.6	92.5	92.5	7.5	2.6	3	87	<0.2	0.8																	
Bottom	9.2	0.0	165	16.6	16.6						8.2	8.2	31.6	31.6	92.5	92.5	7.5	4.5	3	90	<0.2	0.9																	
	9.2	0.0	165	16.6	16.6						8.2	8.2	31.6	31.6	92.5	92.5	7.5	4.6	4	90	<0.2	0.8																	
	C3	Cloudy	Moderate	16:33	11.2						Surface	1.0	0.3	78	17.7	17.7	8.1	8.1	33.2	33.2	97.7	97.7	7.6	7.6	4.0	4.3	8	8	47	49	822096	817793	<0.2			<0.2	0.9	0.7	
												1.0	0.3	74	17.7	8.1	8.1	33.2	33.2	97.7	97.7	7.6	4.0		8		47		<0.2				0.7						
Middle						5.6	0.3	62	17.6	17.6	8.1	8.1	33.2	33.2	97.5	97.5	7.6	4.7	8	49	<0.2	0.7																	
						5.6	0.3	67	17.6	17.6	8.1	8.1	33.2	33.2	97.5	97.5	7.6	4.6	8	48	<0.2	0.7																	
Bottom						10.2	0.3	78	17.6	17.6	8.1	8.1	33.2	33.2	98.0	98.0	7.7	4.4	9	51	<0.2	0.6																	
						10.2	0.3	76	17.6	17.6	8.1	8.1	33.2	33.2	98.0	98.0	7.7	4.4	9	52	<0.2	0.8																	
						IM1	Sunny	Rough	16:19	7.3	Surface	1.0	0.1	178	16.4	16.4	8.2	8.2	32.3	32.3	95.4	95.4	7.7	7.7	7.8	8.7	12	14	83	85			818353	806468	<0.2	<0.2	0.9		0.9
												1.0	0.1	179	16.4	16.4	8.2	8.2	32.3	32.3	95.4	95.4	7.7		7.8		13		83						<0.2		1.0		
Middle	3.7	0.2	197	16.3	16.3						8.2	8.2	32.3	32.3	95.1	95.1	7.7	8.2	15	86	<0.2	0.9																	
	3.7	0.1	196	16.3	16.3						8.2	8.2	32.3	32.3	95.1	95.1	7.7	8.3	14	86	<0.2	0.8																	
Bottom	6.3	0.1	180	16.3	16.3						8.2	8.2	32.3	32.3	95.2	95.2	7.7	10.1	16	87	<0.2	0.9																	
	6.3	0.1	179	16.3	16.3						8.2	8.2	32.3	32.3	95.2	95.2	7.7	10.1	15	87	<0.2	0.9																	
	IM2	Sunny	Rough	16:12	7.4						Surface	1.0	0.1	171	16.4	16.4	8.2	8.2	32.2	32.2	95.5	95.5	7.7	7.7	7.8	10.8	12	11	82	86	819179	806259			<0.2	<0.2	0.7	0.7	
												1.0	0.1	169	16.4	16.4	8.2	8.2	32.2	32.2	95.5	95.5	7.7		7.8		12		83						<0.2		0.6		
Middle						3.7	0.1	175	16.2	16.2	8.2	8.2	32.2	32.2	95.1	95.1	7.7	11.4	11	86	<0.2	0.7																	
						3.7	0.1	177	16.2	16.2	8.2	8.2	32.2	32.2	95.1	95.1	7.7	11.5	11	86	<0.2	0.6																	
Bottom						6.4	0.1	154	16.2	16.2	8.2	8.2	32.2	32.2	95.5	95.5	7.7	13.1	8	90	<0.2	0.6																	
						6.4	0.2	151	16.2	16.2	8.2	8.2	32.2	32.2	95.5	95.5	7.7	13.2	9	90	<0.2	0.7																	
						IM7	Sunny	Rough	15:50	7.9	Surface	1.0	0.2	92	16.6	16.6	8.2	8.2	31.7	31.7	93.3	93.3	7.5	7.5	2.0	3.4	4	4	83	87			821327	806815	<0.2	<0.2	0.8		0.8
												1.0	0.2	85	16.6	16.6	8.2	8.2	31.7	31.7	93.3	93.3	7.5		2.0		5		83						<0.2		0.8		
Middle	4.0	0.1	93	16.5	16.5						8.2	8.2	32.0	32.0	93.0	93.1	7.5	2.8	4	88	<0.2	0.8																	
	4.0	0.1	88	16.5	16.5						8.2	8.2	32.0	32.0	93.2	93.1	7.5	2.9	5	88	<0.2	0.7																	
Bottom	6.9	0.2	101	16.4	16.4						8.2	8.2	32.1	32.1	94.2	94.2	7.6	5.4	4	90	<0.2	0.9																	
	6.9	0.2	102	16.4	16.4						8.2	8.2	32.1	32.1	94.2	94.2	7.6	5.4	4	90	<0.2	0.8																	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; Value exceeding Limit Level is bolded and underlined

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 06 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)				
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	
IM10	Cloudy	Moderate	15:15	7.4	Surface	1.0	0.2	91	17.2	17.2	8.2	8.2	32.8	32.8	102.4	102.4	8.1	8.2	7.6	9.9	9	11	86	87	822240	809861	<0.2	0.7	0.7				
						1.0	0.2	96	17.2	17.2	8.2	32.8	102.4	8.1	7.9	10	85		<0.2		0.7												
					Middle	3.7	0.1	74	17.1	17.1	8.2	8.2	32.8	103.2	8.2	10.8	11	87	<0.2	0.7													
						3.7	0.2	69	17.1	17.1	8.2	8.2	32.8	103.3	8.2	10.8	10	86	<0.2	0.6													
					Bottom	6.4	0.2	81	17.1	17.1	8.2	8.2	32.8	103.9	8.2	11.3	12	90	<0.2	0.8													
						6.4	0.2	87	17.1		8.2	32.8	104.4	8.3	11.2	11	89	<0.2	0.8														
IM11	Cloudy	Moderate	15:22	7.8	Surface	1.0	0.2	78	17.3	17.3	8.1	8.1	32.8	32.8	100.3	100.3	7.9	7.9	5.2	5.8	14	12	85	88	821504	810545	<0.2	0.7	0.8				
						1.0	0.2	72	17.3	17.3	8.1	32.8	100.3	7.9	5.3	14	86		<0.2		0.8												
					Middle	3.9	0.3	99	17.3	17.3	8.1	8.1	32.8	100.4	7.9	5.6	13	87	<0.2	0.7													
						3.9	0.3	105	17.3	17.3	8.1	32.8	100.4	7.9	5.7	13	87	<0.2	0.8														
					Bottom	6.8	0.2	73	17.3	17.3	8.1	8.1	32.8	101.5	8.0	6.6	8	90	<0.2	0.8													
						6.8	0.2	75	17.3	17.3	8.1	32.8	101.9	8.0	6.6	8	91	<0.2	0.7														
IM12	Cloudy	Moderate	15:30	8.3	Surface	1.0	0.3	102	17.3	17.3	8.1	8.1	32.7	32.7	100.5	100.5	7.9	7.9	4.9	5.6	6	8	86	88	821148	811524	<0.2	0.7	0.7				
						1.0	0.3	102	17.3	17.3	8.1	32.8	100.5	7.9	4.9	6	85		<0.2		0.6												
					Middle	4.2	0.3	110	17.2	17.2	8.1	8.1	32.7	100.3	7.9	5.4	8	87	<0.2	0.7													
						4.2	0.3	112	17.2	17.2	8.1	32.7	100.2	7.9	5.5	8	88	<0.2	0.6														
					Bottom	7.3	0.2	70	17.2	17.2	8.1	8.1	32.8	100.3	7.9	6.5	11	90	<0.2	0.6													
						7.3	0.2	76	17.2	17.2	8.1	32.8	100.4	7.9	6.5	11	89	<0.2	0.8														
SR1A	Cloudy	Moderate	15:57	5.6	Surface	1.0	0.0	48	17.3	17.3	8.1	8.1	32.6	32.6	100.0	100.0	7.9	7.9	3.6	3.7	8	8	-	-	819974	812661	-	-	-				
						1.0	0.0	46	17.3	17.3	8.1	32.6	100.0	7.9	3.8	7	-		-		-												
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-		
					Bottom	4.6	0.0	49	17.2	17.2	8.1	8.1	32.6	100.2	7.9	3.6	9	-	-	-	-	-	-	-			-	-		-	-	-	
						4.6	0.1	53	17.2	17.2	8.1	8.1	32.6	100.3	7.9	3.8	8	-	-	-	-	-	-	-			-	-		-	-	-	
SR2	Cloudy	Moderate	16:11	4.3	Surface	1.0	0.2	71	17.3	17.3	8.1	8.1	32.7	32.7	102.0	102.1	8.0	8.1	5.2	5.3	8	9	87	88	821473	814153	<0.2	0.8	0.8				
						1.0	0.2	72	17.3	17.3	8.1	32.8	102.2	8.1	5.2	8	87		<0.2		0.8												
					Middle	-	0.2	74	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-	-	
						-	0.2	71	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-	-	
					Bottom	3.3	0.2	57	17.3	17.3	8.1	8.1	32.7	103.3	8.2	5.4	9	89	<0.2	0.8													
						3.3	0.3	59	17.3	17.3	8.1	8.1	32.7	103.4	8.2	5.4	9	89	<0.2	0.8													
SR3	Sunny	Rough	15:42	8.8	Surface	1.0	0.1	123	16.6	16.6	8.2	8.2	31.5	31.5	93.7	93.7	7.6	7.5	1.3	2.1	3	4	-	-	822169	807585	-	-	-				
						1.0	0.1	123	16.6	16.6	8.2	31.5	93.6	7.5	1.3	4	-		-		-												
					Middle	4.4	0.2	135	16.6	16.6	8.2	8.2	31.7	92.4	7.4	2.7	4	-	-	-	-	-	-	-			-	-		-	-	-	
						4.4	0.2	140	16.6	16.6	8.2	31.7	92.4	7.4	2.7	5	-	-	-	-	-	-	-	-			-	-		-	-		
					Bottom	7.8	0.2	107	16.6	16.6	8.2	8.2	31.8	92.5	7.4	2.4	5	-	-	-	-	-	-	-			-	-		-	-	-	
						7.8	0.2	113	16.6	16.6	8.2	8.2	31.8	92.5	7.4	2.5	5	-	-	-	-	-	-	-			-	-		-	-	-	
SR4A	Sunny	Moderate	17:12	9.1	Surface	1.0	0.0	77	16.4	16.4	8.2	8.2	32.3	32.3	96.3	96.3	7.8	7.8	5.6	6.6	6	5	-	-	817194	807802	-	-	-				
						1.0	0.1	71	16.4	16.4	8.2	32.3	96.3	7.8	5.7	7	-		-		-												
					Middle	4.6	0.0	75	16.4	16.4	8.3	8.3	32.3	96.0	7.7	6.6	4	-	-	-	-	-	-	-			-	-		-	-	-	
						4.6	0.0	79	16.4	16.4	8.3	32.3	96.0	7.7	6.6	4	-	-	-	-	-	-	-	-			-	-		-	-	-	
					Bottom	8.1	0.0	94	16.4	16.4	8.3	8.3	32.3	96.1	7.7	7.5	5	-	-	-	-	-	-	-			-	-		-	-	-	
						8.1	0.0	92	16.4	16.4	8.3	32.3	96.1	7.7	7.5	4	-	-	-	-	-	-	-	-			-	-		-	-	-	
SR8	Cloudy	Moderate	15:35	4.4	Surface	1.0	-	-	17.3	17.3	8.1	8.1	32.7	32.7	103.1	103.2	8.1	8.2	5.5	6.0	6	8	-	-	820371	811643	-	-	-				
						1.0	-	-	17.2	17.2	8.1	32.7	103.2	8.2	5.6	6	-		-		-												
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-	-	
					Bottom	3.4	-	-	17.1	17.1	8.1	8.1	32.7	104.0	8.2	6.3	10	-	-	-	-	-	-	-			-	-		-	-	-	-
						3.4	-	-	17.1	17.1	8.1	32.7	104.2	8.3	6.4	9	-	-	-	-	-	-	-	-			-	-		-	-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 06 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Fine	Rough	10:26	6.8	Surface	1.0	0.3	35	16.2	16.2	8.2	8.2	32.3	32.3	95.1	95.1	7.7		6.8		12		82		815601	804233	<0.2		0.6	
						1.0	0.3	38	16.2		8.2		32.3		95.1		7.7		6.8		12		82				<0.2		0.8	
					Middle	3.4	0.3	31	16.2	16.2	8.2	8.2	32.3	32.3	94.9	94.9	7.7	7.7	6.0	6.8	12	13	86	86			<0.2	<0.2	0.6	0.7
						3.4	0.3	30	16.2		8.2		32.3		94.9		7.7		6.1		13		86				<0.2		0.7	
					Bottom	5.8	0.3	32	16.2	16.2	8.2	8.2	32.3	32.3	94.6	94.6	7.6	7.6	7.4		15		90				<0.2		0.8	
						5.8	0.3	38	16.2		8.2		32.3		94.6		7.6		7.5		16		90				<0.2		0.8	
					Surface	1.0	0.4	347	16.6	16.6	8.2	8.2	31.5	31.5	93.7	93.7	7.6		1.4		7		79				<0.2		0.9	
						1.0	0.4	349	16.6	16.6	8.2	8.2	31.5	31.5	93.7	93.7	7.5	7.5	1.4		6		79				<0.2		0.7	
C2	Fine	Rough	11:46	8.9	Middle	4.5	0.5	352	16.6	16.6	8.2	8.2	31.6	31.6	92.7	92.7	7.5		2.0	1.9	8	10	86	86	825662	806954	<0.2	<0.2	0.9	0.9
						4.5	0.4	345	16.6	16.6	8.2		31.6		92.7		7.5		2.0		9		87				<0.2	<0.2	0.9	
					Bottom	7.9	0.4	6	16.6	16.6	8.2	8.2	31.6	31.6	93.3	93.3	7.5	7.5	2.3		16		91				<0.2		0.9	
						7.9	0.4	11	16.6	16.6	8.2	8.2	31.6		93.3		7.5		2.3		15		91				<0.2		0.8	
					Surface	1.0	0.3	260	17.4	17.4	8.0	8.0	32.9	32.9	99.3	99.3	7.8		4.7		7		86				<0.2		0.6	
						1.0	0.3	259	17.4		8.0		32.9		99.3		7.8	7.8	4.9		8		85				<0.2		0.7	
C3	Cloudy	Moderate	09:35	11.8	Middle	5.9	0.3	262	17.4	17.4	8.0	8.0	32.9	32.9	98.9	99.0	7.8		6.0	6.8	12	10	87	87	822131	817807	<0.2	<0.2	0.8	0.7
						5.9	0.4	257	17.4		8.0		32.9		99.0		7.8		6.2		11		87				<0.2	<0.2	0.7	
					Bottom	10.8	0.4	274	17.4	17.4	8.0	8.0	32.9	32.9	100.2	100.4	7.9	7.9	9.5		12		89				<0.2		0.8	
						10.8	0.3	273	17.4		8.0		32.9		100.5		7.9		9.8		12		90				<0.2		0.8	
					Surface	1.0	0.2	22	16.3	16.3	8.2	8.2	32.2	32.2	95.4	95.4	7.7		7.3		14		82				<0.2		0.9	
IM1	Fine	Moderate	10:48	6.9	Surface	1.0	0.2	23	16.3	16.3	8.2		32.2		95.4		7.7	7.7	7.3		13		82		818359	806435	<0.2	<0.2	0.9	0.9
						1.0	0.2	5	16.3	16.3	8.2	8.2	32.2	32.2	95.2	95.2	7.7		7.3		17	17	86	86			<0.2	<0.2	0.9	
					Middle	3.5	0.2	24	16.3	16.3	8.2	8.2	32.2	32.2	95.2		7.7	7.7	8.2	8.3	18		86				<0.2	<0.2	0.9	
						3.5	0.2	20	16.3	16.3	8.2		32.2		95.2		7.7		8.2		17		86				<0.2	<0.2	0.9	
					Bottom	5.9	0.2	8	16.2	16.2	8.2	8.2	32.2	32.2	95.5	95.6	7.7	7.7	9.3		19		91				<0.2		0.9	
IM2	Fine	Moderate	10:54	7.3	Surface	1.0	0.2	10	16.3	16.3	8.2	8.2	32.0	32.0	95.2	95.2	7.7		7.9		12		79		819161	806253	<0.2	<0.2	0.8	
						1.0	0.2	5	16.3	16.3	8.2		32.0		95.2		7.7	7.7	7.9		11		79				<0.2	<0.2	0.9	0.9
					Middle	3.7	0.2	4	16.2	16.2	8.2	8.2	32.1	32.1	94.7	94.7	7.7		8.3	8.5	12	11	86	86			<0.2	<0.2	0.8	
						3.7	0.2	4	16.2		8.2		32.1		94.7		7.7		8.3		11		86				<0.2	<0.2	0.8	
					Bottom	6.3	0.2	6	16.2	16.2	8.2	8.2	32.2	32.2	95.0		7.7	7.7	9.2		10		90				<0.2	<0.2	0.9	
						6.3	0.2	5	16.2	16.2	8.2	8.2	32.2	32.2	95.1	95.1	7.7	7.7	9.3		10		90				<0.2	<0.2	1.0	
					Surface	1.0	0.2	342	16.6	16.6	8.2	8.2	31.8	31.8	93.0	93.0	7.5		2.0		4		82		821334	806833	<0.2	<0.2	0.9	0.9
						1.0	0.3	339	16.6	16.6	8.2		31.8		93.0		7.5	7.5	2.0		3		82				<0.2	<0.2	0.9	
IM7	Fine	Rough	11:14	7.8	Middle	3.9	0.2	334	16.6	16.6	8.2	8.2	31.9	31.9	92.3	92.3	7.4		3.2	3.2	4	4	86	86			<0.2	<0.2	1.1	0.9
						3.9	0.2	331	16.6	16.6	8.2		31.9		92.3		7.4		3.3		5		86				<0.2	<0.2	1.0	
					Bottom	6.8	0.2	327	16.6	16.6	8.2	8.2	32.0	32.0	92.4		7.4	7.4	4.2		5		90				<0.2	<0.2	0.8	
						6.8	0.2	328	16.6	16.6	8.2		32.0		92.5		7.4	7.4	4.2		5		90				<0.2	<0.2	0.8	
					Surface	1.0	0.2	342	16.6	16.6	8.2	8.2	31.8	31.8	93.0	93.0	7.5		2.0		4		82				<0.2	<0.2	0.9	0.9
						1.0	0.3	339	16.6	16.6	8.2		31.8		93.0		7.5	7.5	2.0		3		82				<0.2	<0.2	0.9	
					Middle	3.9	0.2	334	16.6	16.6	8.2	8.2	31.9	31.9	92.3	92.3	7.4		3.2	3.2	4	4	86	86			<0.2	<0.2	1.1	0.9
						3.9	0.2	331	16.6	16.6	8.2		31.9		92.3		7.4		3.3		5		86				<0.2	<0.2	1.0	
					Bottom	6.8	0.2	327	16.6	16.6	8.2	8.2	32.0	32.0	92.4		7.4	7.4	4.2		5		90				<0.2	<0.2	0.8	
						6.8	0.2	328	16.6	16.6	8.2		32.0		92.5		7.4	7.4	4.2		5		90				<0.2	<0.2	0.8	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 06 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)													
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA										
IM10	Cloudy	Moderate	11:00	7.4	Surface	1.0	0.4	274	16.9	16.9	8.1	8.1	32.6	32.6	102.4	102.4	8.1	8.2	7.3	7.9	8	7	86	88	822262	809822	<0.2	<0.2	0.7	0.8												
						1.0	0.4	278	16.9		8.1		32.6		102.4		8.1												7.4			9		85		<0.2	0.8					
					Middle	3.7	0.4	274	16.9	16.9	8.1	8.1	32.7	32.7	102.6	102.6	8.2												8.1			6		87		<0.2	0.8					
						3.7	0.4	271	16.9		8.1		32.7		102.6		8.2												8.1			7		87		<0.2	0.7					
					Bottom	6.4	0.4	289	16.9	16.9	8.1	8.1	32.7	32.7	103.2		8.2										8.2		8.4			6		90		<0.2	0.8					
						6.4	0.4	293	16.9	16.9	8.1		32.7	32.7	103.4	103.3	8.2										8.2		8.3			5		91		<0.2	0.8					
IM11	Cloudy	Moderate	10:53	7.9	Surface	1.0	0.4	292	17.0	17.0	8.1	8.1	32.7	32.7	101.7	101.7	8.1	8.1	7.3	8.6	5	6	86	88	821515	810551	<0.2	<0.2	0.7	0.7												
						1.0	0.5	297	17.0		8.1		32.7		101.7		8.1												7.4			5		85		<0.2	0.7					
					Middle	4.0	0.5	259	17.0	17.0	8.1	8.1	32.7	32.7	101.8	101.8	8.1												7.9			6		88		<0.2	0.7					
						4.0	0.5	251	17.0		8.1		32.7		101.8		8.1												8.0			6		87		<0.2	0.8					
					Bottom	6.9	0.4	271	16.9	16.9	8.1	8.1	32.7	32.7	102.3	102.4	8.1										8.1		10.6			7		90		<0.2	0.7					
						6.9	0.4	266	16.9		8.1		32.7	32.7	102.4		8.1												10.5			6		91		<0.2	0.8					
IM12	Cloudy	Moderate	10:46	8.5	Surface	1.0	0.4	281	17.0	17.0	8.1	8.1	32.7	32.7	101.2	101.2	8.0	8.0	11.5	13.8	16	17	85	87	821184	811508	<0.2	<0.2	0.8	0.7												
						1.0	0.5	274	17.0		8.1		32.7		101.2		8.0												11.6			17		85		<0.2	0.6					
					Middle	4.3	0.5	281	17.0	17.0	8.1	8.1	32.7	32.7	101.2	101.2	8.0												12.6			17		87		<0.2	0.6					
						4.3	0.4	278	17.0		8.1		32.7		101.2		8.0												13.1			16		87		<0.2	0.7					
					Bottom	7.5	0.5	278	16.9	16.9	8.1	8.1	32.7	32.7	101.3	101.4	8.1										8.1		17.3			18		90		<0.2	0.8					
						7.5	0.5	281	16.9		8.1		32.7	32.7	101.4		8.1												16.6			18		90		<0.2	0.8					
SR1A	Cloudy	Moderate	10:16	5.7	Surface	1.0	0.0	180	17.1	17.1	8.1	8.1	32.7	32.7	100.2	100.3	7.9	7.9	6.9	7.9	4	5	-	-	819979	812656	-	-	-	-												
						1.0	0.1	179	17.1		8.1		32.7	32.7	100.3		7.9												7.3			5		-		-		-				
					Middle	-	-	-	-	-	-	-	-	-	-	-	-										-		-			-		-		-	-	-	-	-	-	
						-	-	-	-		-		-		-		-												-			-		-		-	-	-	-	-		
					Bottom	4.7	0.0	195	17.1	17.1	8.1	8.1	32.7	32.7	102.9	103.4	8.2										8.2		8.5			8		-		-		-		-	-	-
						4.7	0.1	195	17.1	17.1	8.1	8.1	32.7	32.7	103.9		8.2												9.1			7		-		-		-		-	-	-
SR2	Cloudy	Moderate	10:03	4.7	Surface	1.0	0.1	246	17.1	17.1	8.1	8.1	32.7	32.7	101.7	101.8	8.1	8.1	6.2	6.3	10	10	85	87	821466	814174	<0.2	<0.2	0.8	0.8												
						1.0	0.1	247	17.1		8.1		32.7		101.8		8.1												6.2			10		86		<0.2	0.7					
					Middle	-	0.1	272	-	-	-	-	-	-	-	-	-										-		-			-		-		-		-	-	-	-	
						-	0.1	276	-		-		-		-		-												-			-		-		-		-	-	-	-	
					Bottom	3.7	0.1	247	17.0	17.0	8.1	8.1	32.7	32.7	103.0	103.1	8.2										8.2		6.5			8		89		<0.2	0.8					
						3.7	0.1	248	17.0	17.0	8.1		32.7	32.7	103.2		8.2												6.5			7		89		<0.2	0.8					
SR3	Fine	Rough	11:22	8.3	Surface	1.0	0.4	353	16.6	16.6	8.2	8.2	31.5	31.5	94.3	94.3	7.6	7.5	1.2	2.4	3	5	-	-	822127	807558	-	-	-	-												
						1.0	0.4	347	16.6		8.2		31.5		94.3												7.6				1.2		4		-		-		-			
					Middle	4.2	0.3	352	16.6	16.6	8.2	8.2	31.9	31.9	92.0		92.0										7.4				2.9		5		-		-		-		-	-
						4.2	0.3	356	16.6		8.2		31.9		92.0												7.4				2.9		6		-		-		-		-	-
					Bottom	7.3	0.3	326	16.7	16.7	8.2	8.2	31.9	31.9	92.1		92.2										7.4		7.4		3.2		5		-		-		-		-	-
						7.3	0.3	327	16.7	16.7	8.2	8.2	31.9	31.9	92.2		92.2										7.4		7.4		3.2		6		-		-		-		-	-
SR4A	Fine	Moderate	10:09	8.5	Surface	1.0	0.0	253	16.4	16.4	8.1	8.1	32.0	32.0	93.3	93.3	7.5	7.5	3.9	4.3	9	-	-	817177	807818	-	-	-	-													
						1.0	0.0	249	16.4		8.1		32.0		93.3											7.5				3.9		8		-		-		-				
					Middle	4.3	0.1	256	16.4	16.4	8.1	8.1	32.0	32.0	93.0		93.0									7.5				4.3		8		-		-		-	-	-		
						4.3	0.1	253	16.4		8.1		32.0		93.0											7.5				4.3		8		-		-		-	-	-		
					Bottom	7.5	0.0	231	16.3	16.3	8.1	8.1	32.0	32.0	93.1		93.1									7.5		7.5		4.5		10		-		-		-		-	-	
						7.5	0.0	225	16.3		8.1		32.0		93.1													7.5			4.6		10		-		-		-		-	-
SR8	Cloudy	Moderate	10:39	4.6	Surface	1.0	-	-	17.0	17.0	8.2	8.2	32.7	32.7	101.9	101.9	8.1	8.1	4.7	9.2	7	-	-	820396	811601	-	-	-	-													
						1.0	-	-	17.0		8.2		32.7		101.9											8.1				9.1		6		-		-		-				
					Middle	-	-	-	-	-	-	-	-	-	-		-									-		-		-		-		-		-		-	-	-	-	
						-	-	-	-		-		-		-											-				-		-		-		-		-	-	-		
					Bottom	3.6	-	-	17.0	17.0	8.6	8.7	32.5	32.5	102.8		102.9									8.2		8.2		8.9		12		-		-		-		-	-	-
						3.6	-	-	17.0		8.7		32.5		102.9													8.2		8.2	9.8		13		-		-		-		-	-

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 08 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)			
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA
C1	Cloudy	Moderate	04:31	7.8	Surface	1.0	0.1	207	16.6	16.6	8.2	8.2	32.5	32.5	96.7	96.7	7.8	7.8	1.9	2.7	5	5	46	49	815642	804229	<0.2	<0.2	0.6	0.4		
						1.0	0.2	202	16.6	16.6	8.2	8.2	32.5	32.5	96.7	96.7	7.8		1.9		4		46				<0.2		0.4			
					Middle	3.9	0.1	227	16.6	16.6	8.2	8.2	32.6	32.6	96.3	96.3	7.7	7.7	2.4	7.7	4	5	49	51			<0.2		0.3			
						3.9	0.1	226	16.6	16.6	8.2	8.2	32.6	32.6	96.3	96.3	7.7		2.4		5		49				<0.2		0.4			
					Bottom	6.8	0.1	231	16.7	16.7	8.2	8.2	32.7	32.7	95.9	95.9	7.7	7.7	3.8	7.7	5	6	51	51			<0.2		0.4			
						6.8	0.1	234	16.7		8.2	8.2	32.7	32.7	95.9	95.9	7.7		3.8		6		51				<0.2		0.3			
C2	Cloudy	Moderate	06:07	11.5	Surface	1.0	0.4	174	16.7	16.7	8.2	8.2	31.0	31.0	96.4	96.4	7.8	7.7	1.5	3.6	4	3	46	48	825668	806932	<0.2	<0.2	0.8	0.8		
						1.0	0.4	170	16.7	16.7	8.2	8.2	31.0	31.0	96.3	96.4	7.8		1.5		3		46				<0.2		0.8			
					Middle	5.8	0.4	176	16.8	16.8	8.2	8.2	31.7	31.7	95.3	95.3	7.6	7.6	1.6	7.6	2	3	48	49			<0.2		0.9			
						5.8	0.4	177	16.8	16.8	8.2	8.2	31.7	31.7	95.3	95.3	7.6		1.6		3		49				<0.2		0.9			
					Bottom	10.5	0.4	190	16.7	16.7	8.2	8.2	31.8	31.8	94.5	94.5	7.6	7.6	7.9	7.6	2	3	50	51			<0.2		0.8			
						10.5	0.4	194	16.7	16.7	8.2	8.2	31.8	31.8	94.5	94.5	7.6		7.9		3		51				<0.2		0.7			
C3	Cloudy	Moderate	03:37	11.0	Surface	1.0	0.1	89	17.5	17.5	8.1	8.1	33.1	33.1	99.0	99.0	7.8	7.8	3.2	3.3	4	3	47	48	822120	817814	<0.2	<0.2	0.7	1.1		
						1.0	0.1	90	17.5	17.5	8.1	8.1	33.1	33.1	99.0	99.0	7.8		3.3		3		46				<0.2		0.8			
					Middle	5.5	0.1	93	17.5	17.5	8.0	8.0	33.1	33.1	98.6	98.6	7.7	7.7	3.4	7.7	3	3	47	48			<0.2		0.7			
						5.5	0.2	95	17.5	17.5	8.0	8.0	33.1	33.1	98.5	98.5	7.7		3.4		3		48				<0.2		0.7			
					Bottom	10.0	0.1	110	17.5	17.5	8.0	8.0	33.0	33.0	98.4	98.5	7.7	7.7	3.3	7.7	3	2	50	52			<0.2		1.8			
						10.0	0.1	109	17.5	17.5	8.0	8.0	33.0	33.0	98.5	98.5	7.7		3.5		2		52				<0.2		1.9			
IM1	Cloudy	Moderate	04:51	6.2	Surface	1.0	0.1	196	16.5	16.5	8.2	8.2	32.1	32.1	96.4	96.4	7.8	7.8	1.2	2.9	4	4	45	48	818363	806465	<0.2	<0.2	0.6	0.5		
						1.0	0.1	203	16.5	16.5	8.2	8.2	32.1	32.1	96.4	96.4	7.8		1.2		3		46				<0.2		0.5			
					Middle	3.1	0.2	172	16.5	16.5	8.3	8.3	32.5	32.5	96.8	96.8	7.8	7.8	2.0	7.8	4	4	48	48			<0.2		0.6			
						3.1	0.1	168	16.5	16.5	8.3	8.3	32.5	32.5	96.8	96.8	7.8		2.0		4		48				<0.2		0.4			
					Bottom	5.2	0.2	206	16.6	16.6	8.3	8.3	32.6	32.6	96.8	96.8	7.8	7.8	5.5	7.8	6	5	50	50			<0.2		0.5			
						5.2	0.2	198	16.6	16.6	8.3	8.3	32.6	32.6	96.8	96.8	7.8		5.6		5		50				<0.2		0.6			
IM2	Cloudy	Moderate	04:58	7.1	Surface	1.0	0.1	185	16.5	16.5	8.2	8.2	32.2	32.2	96.3	96.3	7.7	7.7	1.3	2.0	4	4	45	48	819178	806246	<0.2	<0.2	0.5	0.5		
						1.0	0.2	182	16.5	16.5	8.2	8.2	32.2	32.2	96.3	96.3	7.7		1.3		3		45				<0.2		0.6			
					Middle	3.6	0.1	197	16.5	16.5	8.3	8.3	32.4	32.4	96.3	96.3	7.7	7.7	1.3	7.7	3	4	48	48			<0.2		0.5			
						3.6	0.1	204	16.5	16.5	8.3	8.3	32.4	32.4	96.3	96.3	7.7		1.3		4		48				<0.2		0.6			
					Bottom	6.1	0.2	166	16.5	16.5	8.3	8.3	32.5	32.5	96.4	96.4	7.7	7.7	3.4	7.7	4	4	50	50			<0.2		0.4			
						6.1	0.2	170	16.5	16.5	8.3	8.3	32.5	32.5	96.4	96.4	7.7		3.4		4		50				<0.2		0.5			
IM7	Cloudy	Moderate	05:31	8.3	Surface	1.0	0.1	189	16.6	16.6	8.2	8.2	31.6	31.6	96.2	96.2	7.7	7.7	0.7	0.9	3	3	45	47	821359	806821	<0.2	<0.2	0.7	0.7		
						1.0	0.1	184	16.6	16.6	8.2	8.2	31.6	31.6	96.2	96.0	7.7		0.7		3		45				<0.2		0.7			
					Middle	4.2	0.1	172	16.6	16.6	8.2	8.2	31.7	31.7	96.0	96.0	7.7	7.7	0.7	7.7	4	3	47	47			<0.2		0.6			
						4.2	0.1	167	16.6	16.6	8.2	8.2	31.7	31.7	96.0	96.0	7.7		0.7		3		47				<0.2		0.6			
					Bottom	7.3	0.1	200	16.5	16.5	8.2	8.2	31.9	31.9	95.2	95.3	7.7	7.7	1.4	7.7	2	2	50	49			<0.2		0.7			
						7.3	0.1	206	16.5	16.5	8.2	8.2	31.9	31.9	95.3	95.3	7.7		1.4		2		49				<0.2		0.7			

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 08 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)										
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA							
IM10	Cloudy	Moderate	04:58	7.7	Surface	1.0	0.2	109	17.2	17.2	8.1	8.1	32.4	32.4	102.5	102.5	8.1	8.1	3.2	3.7	2	3	46	48	822230	809824	<0.2	<0.2	0.6	0.8									
						1.0	0.3	116	17.2	8.1	8.1	32.4	32.5	102.5	102.1	8.1	3.2		3		47		<0.2				0.6												
					Middle	3.9	0.3	101	17.2	8.1	8.1	32.5	32.5	102.1	102.1	8.1	3.8		3		47		<0.2				0.7												
						3.9	0.3	96	17.2	8.1	8.1	32.5	32.5	102.1	102.1	8.1	3.9		2		48		<0.2				0.7												
					Bottom	6.7	0.3	107	17.2	8.1	8.1	32.5	32.5	102.3	102.3	8.1	4.1		2		51		<0.2				1.2												
						6.7	0.2	109	17.2	8.1	8.1	32.5	32.5	102.3	102.3	8.1	4.0		3		51		<0.2				1.0												
IM11	Cloudy	Moderate	04:52	7.4	Surface	1.0	0.2	80	17.2	17.2	8.1	8.1	32.5	32.5	102.5	102.5	8.1	8.1	2.9	3.2	2	2	46	48	821511	810557	0.2	0.2	1.1	1.1									
						1.0	0.2	72	17.2	8.1	8.1	32.5	32.6	102.5	102.4	8.1	2.9		3		47		0.2				1.0												
					Middle	3.7	0.3	72	17.2	8.1	8.1	32.6	32.6	102.4	102.4	8.1	3.1		<2		48		<0.2				1.0												
						3.7	0.2	74	17.2	8.1	8.1	32.6	32.6	102.4	102.4	8.1	3.2		<2		48		<0.2				1.1												
					Bottom	6.4	0.2	68	17.2	8.1	8.1	32.7	32.7	102.7	102.7	8.1	3.6		<2		50		<0.2				1.0												
						6.4	0.2	67	17.2	8.1	8.1	32.7	32.7	102.7	102.7	8.1	3.7		<2		51		<0.2				1.1												
IM12	Cloudy	Moderate	04:40	8.0	Surface	1.0	0.2	113	17.2	17.2	8.1	8.1	32.5	32.5	101.8	101.8	8.1	8.1	3.0	4.5	2	2	46	48	821146	811498	0.3	0.2	1.1	1.0									
						1.0	0.3	106	17.2	8.1	8.1	32.5	32.6	101.8	101.5	8.1	3.0		3		47		0.3				1.1												
					Middle	4.0	0.3	100	17.2	8.1	8.1	32.6	32.6	101.5	101.5	8.0	4.1		2		48		<0.2				0.9												
						4.0	0.2	100	17.2	8.1	8.1	32.6	32.6	101.5	101.5	8.0	4.2		2		47		<0.2				0.9												
					Bottom	7.0	0.3	97	17.2	8.1	8.1	32.7	32.7	102.9	103.0	8.1	6.2		<2		50		<0.2				1.1												
						7.0	0.3	102	17.2	8.1	8.1	32.7	32.7	103.1	103.1	8.1	6.3		<2		51		<0.2				1.1												
SR1A	Cloudy	Moderate	04:13	5.5	Surface	1.0	0.0	72	17.2	17.2	8.1	8.1	32.6	32.6	101.0	101.0	8.0	8.0	3.3	4.7	3	3	-	-	819981	812656	-	-	-	-									
						1.0	0.0	70	17.2	8.1	8.1	32.6	32.6	101.0	101.0	8.0	3.4		4		-		-																
					Middle	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-	-		
					Bottom	4.5	0.0	79	17.3	8.1	8.1	32.9	32.9	100.7	100.7	7.9	6.0		3		-		-				-		-		-	-	-	-	-	-	-	-	-
						4.5	0.0	81	17.3	8.1	8.1	32.9	32.9	100.7	100.7	7.9	6.2		2		-		-				-		-		-	-	-	-	-	-	-	-	
SR2	Cloudy	Moderate	04:00	4.2	Surface	1.0	0.1	50	17.3	17.3	8.1	8.1	32.8	32.8	101.3	101.3	8.0	8.0	3.7	3.8	3	3	47	50	821475	814185	<0.2	<0.2	1.0	1.0									
						1.0	0.1	45	17.3	8.1	8.1	32.8	32.8	101.3	101.3	8.0	3.7		2		49		<0.2				1.1												
					Middle	-	0.1	54	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-	-	-	
						-	0.1	53	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-	-		
					Bottom	3.2	0.1	37	17.3	8.1	8.1	32.8	32.8	101.7	101.7	8.0	4.0		4		52		<0.2				0.9												
						3.2	0.1	37	17.3	8.1	8.1	32.8	32.8	101.7	101.7	8.0	4.0		3		51		<0.2				0.9												
SR3	Cloudy	Moderate	05:41	8.6	Surface	1.0	0.3	157	16.6	16.6	8.2	8.2	31.6	31.6	96.4	96.4	7.8	7.8	0.7	1.1	<2	2	-	-	822139	807592	-	-	-	-									
						1.0	0.3	154	16.6	8.2	8.2	31.6	31.7	96.4	95.6	7.8	0.7		<2		-		-																
					Middle	4.3	0.3	174	16.6	8.2	8.2	31.7	31.7	95.6	95.6	7.7	0.9		<2		-		-				-		-		-	-	-	-	-	-	-		
						4.3	0.3	177	16.6	8.2	8.2	31.7	31.9	95.5	95.5	7.7	0.9		<2		-		-				-		-		-	-	-	-	-	-			
					Bottom	7.6	0.3	176	16.5	8.2	8.2	31.9	31.9	95.9	96.0	7.7	1.6		3		-		-				-		-		-	-	-	-	-	-	-		
						7.6	0.3	176	16.5	8.2	8.2	31.9	31.9	96.0	96.0	7.7	1.6		3		-		-				-		-		-	-	-	-	-	-	-		
SR4A	Cloudy	Calm	04:11	9.0	Surface	1.0	0.0	55	16.7	16.7	8.1	8.1	32.6	32.6	94.7	94.7	7.6	7.6	3.2	3.3	5	6	-	-	817203	807798	-	-	-	-									
						1.0	0.0	48	16.7	8.1	8.1	32.6	32.7	94.7	94.8	7.6	3.2		6		-		-																
					Middle	4.5	0.0	49	16.7	8.1	8.1	32.7	32.7	94.8	94.8	7.6	3.4		6		-		-				-		-		-	-	-	-	-	-			
						4.5	-	53	16.7	8.1	8.1	32.7	32.7	94.8	94.8	7.6	3.4		5		-		-				-		-		-	-	-	-	-	-			
					Bottom	8.0	0.0	42	16.7	8.1	8.1	32.7	32.7	94.8	94.8	7.6	3.2		6		-		-				-		-		-	-	-	-	-	-	-		
						8.0	0.0	48	16.7	8.1	8.1	32.7	32.7	94.8	94.8	7.6	3.2		7		-		-				-		-		-	-	-	-	-	-	-		
SR8	Cloudy	Moderate	04:32	4.4	Surface	1.0	-	-	17.7	17.7	8.1	8.1	32.3	32.3	102.9	103.0	8.1	8.1	4.6	6.7	3	3	-	-	820409	811626	-	-	-	-									
						1.0	-	-	17.7	8.1	8.1	32.3	32.3	103.1	103.1	8.1	5.1		3		-		-																
					Middle	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-		-		-	-	-	-	-	-			
					Bottom	3.4	-	-	17.5	8.1	8.1	32.3	32.3	104.2	104.4	8.2	8.4		3		-		-				-		-		-	-	-	-	-	-	-	-	
						3.4	-	-	17.5	8.1	8.1	32.3	32.3	104.2	104.4	8.2	8.8		4		-		-				-		-		-	-	-	-	-	-	-		

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 08 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Cloudy	Rough	12:27	8.0	Surface	1.0	0.3	33	16.7	16.7	8.3	8.3	32.6	32.6	96.6	96.6	7.7		7.6		13		46		815643	804233	<0.2		0.3	
						1.0	0.3	25	16.7		8.3		32.6		96.6		7.7		7.6		13		46				<0.2		0.4	
					Middle	4.0	0.3	48	16.7	16.7	8.3	8.3	32.6	32.6	96.7	96.7	7.7	7.7	9.7	9.6	15	14	49	49			<0.2	<0.2	0.3	0.4
						4.0	0.2	53	16.7		8.3		32.6		96.7		7.7		9.5		15		49				<0.2		0.4	
					Bottom	7.0	0.3	19	16.7	16.7	8.3	8.3	32.6	32.6	97.0	97.1	7.7	7.8	11.4		14		52				<0.2		0.4	
						7.0	0.3	18	16.7		8.3		32.6		97.1		7.8		11.5		15		52				<0.2		0.4	
					Surface	1.0	0.2	342	16.7	16.7	8.2	8.2	30.9	30.9	96.5	96.5	7.8		2.0		14		46				<0.2		0.8	
						1.0	0.2	345	16.7	16.7	8.2	8.2	30.9	30.9	96.5	96.5	7.8	7.7	2.0		14		47				<0.2		0.8	
C2	Cloudy	Moderate	11:08	11.7	Middle	5.9	0.2	325	16.8	16.8	8.2	8.2	31.7	31.7	95.0	95.0	7.6		2.1	3.4	10	12	49	49	825669	806927	<0.2	<0.2	1.1	1.0
						5.9	0.2	332	16.8		8.2		31.7		94.9		7.6		2.1		11		50				<0.2	<0.2	1.1	
					Bottom	10.7	0.2	4	16.7	16.7	8.2	8.2	31.8	31.8	94.4	94.4	7.6	7.6	6.1		10		51				<0.2		0.9	
						10.7	0.2	359	16.7		8.2		31.8		94.4		7.6		6.2		11		51				<0.2		1.0	
					Surface	1.0	0.4	266	17.6	17.6	8.1	8.1	33.3	33.3	96.6	96.6	7.5		3.6		4		47				<0.2		1.4	
						1.0	0.4	265	17.6		8.1		33.3		96.6		7.6	7.6	3.7		3		48				<0.2		1.4	
					Middle	5.9	0.3	241	17.6	17.6	8.1	8.1	33.3	33.3	97.2	97.6	7.7		4.8	4.4	3	3	48	49			<0.2	<0.2	1.3	1.2
						5.9	0.3	238	17.6		8.1		33.3		97.9		7.7		4.8		3		50				<0.2	<0.2	1.2	
C3	Cloudy	Moderate	12:59	11.8	Bottom	10.8	0.4	249	17.6	17.6	8.1	8.1	33.2	33.2	99.7	99.8	7.8	7.8	4.9		3		51		822094	817795	<0.2		0.8	1.2
						10.8	0.5	251	17.6		8.1		33.2		99.8		7.8		4.9		3		52				<0.2		1.0	
					Surface	1.0	0.2	12	16.7	16.7	8.3	8.3	32.7	32.7	97.7	97.7	7.8		3.9		7		46				<0.2		0.4	
						1.0	0.1	19	16.7		8.3		32.7		97.7		7.8	7.8	3.9		7		45				<0.2		0.4	
					Middle	3.2	0.1	25	16.6	16.6	8.3	8.3	32.7	32.7	97.4	97.4	7.8		4.2	4.5	8	12	48	48			<0.2	<0.2	0.4	0.4
						3.2	0.1	23	16.6		8.3		32.7		97.4		7.8		4.2		9		48				<0.2	<0.2	0.4	
					Bottom	5.4	0.1	4	16.6	16.6	8.3	8.3	32.7	32.7	97.8	97.8	7.8	7.8	5.4		19		50				<0.2		0.4	
						5.4	0.1	7	16.6		8.3		32.7		97.8		7.8		5.4		19		51				<0.2		0.4	
IM2	Cloudy	Moderate	11:59	7.6	Surface	1.0	0.1	357	16.8	16.8	8.3	8.3	32.6	32.6	96.3	96.3	7.7		4.7		7		45		819166	806240	<0.2		0.3	
						1.0	0.2	359	16.8		8.3		32.6		96.3		7.7	7.7	4.7		8		45				<0.2		0.4	
					Middle	3.8	0.2	9	16.7	16.7	8.3	8.3	32.6	32.6	96.9	96.9	7.7		5.3	6.4	8	9	49	48			<0.2	<0.2	0.4	0.4
						3.8	0.1	6	16.7		8.3		32.6		96.9		7.7		5.3		7		49				<0.2		0.4	
					Bottom	6.6	0.1	12	16.6	16.6	8.3	8.3	32.6	32.6	97.4	97.4	7.8	7.8	9.2		11		51				<0.2	<0.2	0.4	
						6.6	0.1	15	16.6		8.3		32.6		97.4		7.8		9.4		12		50				<0.2		0.4	
					Surface	1.0	0.2	302	16.6	16.6	8.2	8.2	31.6	31.6	96.9	96.9	7.8		0.6		2		45				<0.2		0.7	
						1.0	0.2	302	16.6		8.2		31.6		96.9		7.8	7.8	0.6		3		45				<0.2		0.8	
IM7	Cloudy	Moderate	11:36	8.3	Middle	4.2	0.2	283	16.6	16.6	8.2	8.2	31.6	31.6	96.6	96.6	7.8		0.7	0.9	4	3	48	48	821360	806846	<0.2	<0.2	0.5	0.6
						4.2	0.1	287	16.6	16.6	8.2	8.2	31.6	31.6	96.6	96.6	7.8		0.7		3		48				<0.2	<0.2	0.6	
					Bottom	7.3	0.1	313	16.6	16.6	8.2	8.2	31.7	31.7	96.2	96.2	7.8	7.8	1.4		3		50				<0.2		0.5	
						7.3	0.1	315	16.6		8.2		31.7		96.2		7.8		1.4		4		50				<0.2		0.7	
					Surface	1.0	0.2	302	16.6	16.6	8.2	8.2	31.6	31.6	96.9	96.9	7.8		0.6		2		45				<0.2		0.7	
						1.0	0.2	302	16.6		8.2		31.6		96.9		7.8	7.8	0.6		3		45				<0.2		0.8	
					Middle	4.2	0.2	283	16.6	16.6	8.2	8.2	31.6	31.6	96.6	96.6	7.8		0.7		4		48				<0.2		0.5	
						4.2	0.1	287	16.6	16.6	8.2	8.2	31.6	31.6	96.6	96.6	7.8		0.7		3		48				<0.2		0.6	
					Bottom	7.3	0.1	313	16.6	16.6	8.2	8.2	31.7	31.7	96.2	96.2	7.8	7.8	1.4		3		50				<0.2		0.5	
						7.3	0.1	315	16.6		8.2		31.7		96.2		7.8		1.4		4		50				<0.2		0.7	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 08 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)					
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA		
IM10	Cloudy	Moderate	11:36	7.0	Surface	1.0	0.3	267	17.2	17.2	8.1	8.1	32.6	32.6	102.2	102.2	8.1	8.1	4.7	5.1	3	2	47	49	822216	809850	<0.2	<0.2	0.7	0.9				
						1.0	0.2	262	17.2	17.2	8.1	8.1	32.6	102.2	8.1	4.7	3		47		<0.2		0.7											
					Middle	3.5	0.4	296	17.2	17.2	8.1	8.1	32.6	102.5	102.6	8.1	5.1	2	49	<0.2	0.7													
						3.5	0.4	301	17.2	17.2	8.1	8.1	32.6	102.6	102.6	8.1	5.2	2	48	<0.2	0.6													
					Bottom	6.0	0.3	261	17.2	17.2	8.2	8.2	32.5	103.3	103.4	8.2	5.3	2	51	<0.2	1.2													
						6.0	0.4	261	17.2	17.2	8.2	8.2	32.5	103.4	103.4	8.2	5.4	2	52	<0.2	1.2													
IM11	Cloudy	Moderate	11:48	8.2	Surface	1.0	0.4	263	17.2	17.2	8.1	8.1	32.7	32.7	101.5	101.5	8.0	8.0	5.1	6.0	2	2	46	49	821481	810558	<0.2	<0.2	1.8	1.7				
						1.0	0.4	270	17.2	17.2	8.1	8.1	32.7	101.5	8.0	5.2	3		47		<0.2		1.7											
					Middle	4.1	0.4	280	17.2	17.2	8.1	8.1	32.6	101.6	101.6	8.0	5.4	2	49	<0.2	1.7													
						4.1	0.4	283	17.2	17.2	8.1	8.1	32.6	101.6	101.6	8.0	5.5	3	48	<0.2	1.8													
					Bottom	7.2	0.4	256	17.2	17.2	8.1	8.1	32.6	102.3	102.4	8.1	7.3	<2	51	<0.2	1.6													
						7.2	0.3	260	17.2	17.2	8.1	8.1	32.6	102.4	102.4	8.1	7.4	<2	52	<0.2	1.7													
IM12	Cloudy	Moderate	11:56	8.6	Surface	1.0	0.4	280	17.3	17.3	8.1	8.1	32.9	32.9	100.9	100.9	7.9	8.0	6.2	7.3	2	2	47	49	821149	811500	<0.2	<0.2	0.9	1.0				
						1.0	0.4	277	17.3	17.3	8.1	8.1	32.9	100.9	8.0	6.4	2		47		<0.2		0.8											
					Middle	4.3	0.3	276	17.3	17.3	8.1	8.1	32.9	101.1	101.2	8.0	6.5	<2	48	<0.2	1.1													
						4.3	0.4	273	17.3	17.3	8.1	8.1	32.9	101.2	101.2	8.0	7.2	<2	49	<0.2	1.1													
					Bottom	7.6	0.4	265	17.3	17.3	8.1	8.1	32.9	101.7	101.8	8.0	8.7	<2	51	<0.2	1.1													
						7.6	0.4	258	17.3	17.3	8.1	8.1	32.9	101.8	101.8	8.0	8.9	<2	52	<0.2	1.0													
SR1A	Cloudy	Moderate	12:22	5.3	Surface	1.0	0.0	199	17.4	17.4	8.1	8.1	32.8	32.8	101.8	101.9	8.0	8.0	4.4	4.2	2	3	-	-	819983	812653	-	-	-	-				
						1.0	-	199	17.4	17.4	8.1	8.1	32.8	102.0	8.0	4.4	3		-		-		-											
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	4.3	0.0	173	17.3	17.3	8.1	8.1	32.8	102.9	103.1	8.1	4.0	2	-	-	-	-	-	-			-		-		-	-	-	-
						4.3	-	172	17.4	17.4	8.1	8.1	32.8	103.3	103.3	8.1	4.0	3	-	-	-	-	-	-			-		-		-	-	-	-
SR2	Cloudy	Moderate	12:36	4.6	Surface	1.0	0.0	242	17.4	17.4	8.1	8.1	33.0	33.0	101.0	101.0	7.9	7.9	3.3	3.2	2	2	47	49	821463	814175	<0.2	<0.2	1.4	1.4				
						1.0	0.0	239	17.4	17.4	8.1	8.1	33.0	101.0	7.9	3.3	3		48		<0.2		1.3											
					Middle	-	0.0	240	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-
						-	-	245	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	3.6	0.1	249	17.4	17.4	8.1	8.1	33.0	101.1	101.1	7.9	3.2	<2	51	<0.2	1.4													
						3.6	0.1	255	17.4	17.4	8.1	8.1	33.0	101.1	101.1	7.9	3.2	<2	50	<0.2	1.5													
SR3	Cloudy	Moderate	11:28	8.8	Surface	1.0	0.1	315	16.6	16.6	8.2	8.2	31.7	31.7	96.3	96.3	7.8	7.8	1.1	1.0	4	4	-	-	822147	807573	-	-	-	-				
						1.0	0.1	315	16.6	16.6	8.2	8.2	31.7	96.3	7.8	1.1	4		-		-		-											
					Middle	4.4	0.2	330	16.6	16.6	8.2	8.2	31.7	96.1	96.1	7.7	1.0	4	-	-	-	-	-	-			-		-		-	-	-	
						4.4	0.1	336	16.6	16.6	8.2	8.2	31.7	96.1	96.1	7.7	1.0	4	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	7.8	0.2	303	16.6	16.6	8.3	8.3	31.7	96.5	96.5	7.8	1.0	3	-	-	-	-	-	-			-		-		-	-	-	-
						7.8	0.1	306	16.6	16.6	8.3	8.3	31.7	96.5	96.5	7.8	1.0	3	-	-	-	-	-	-			-		-		-	-	-	-
SR4A	Cloudy	Calm	12:47	9.1	Surface	1.0	0.0	240	16.7	16.7	8.3	8.3	32.7	32.7	96.5	96.5	7.7	7.7	7.4	9.0	12	14	-	-	817202	807815	-	-	-	-				
						1.0	0.1	245	16.7	16.7	8.3	8.3	32.7	96.5	7.7	7.4	13		-		-		-											
					Middle	4.6	0.0	221	16.7	16.7	8.3	8.3	32.7	96.4	96.4	7.7	8.7	12	-	-	-	-	-	-			-		-		-	-	-	
						4.6	0.1	220	16.7	16.7	8.3	8.3	32.7	96.4	96.4	7.7	8.6	13	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	8.1	0.0	235	16.7	16.7	8.3	8.3	32.7	96.5	96.5	7.7	11.0	15	-	-	-	-	-	-			-		-		-	-	-	-
						8.1	0.0	229	16.7	16.7	8.3	8.3	32.7	96.5	96.5	7.7	11.1	16	-	-	-	-	-	-			-		-		-	-	-	-
SR8	Cloudy	Moderate	12:01	4.6	Surface	1.0	-	-	17.3	17.3	8.1	8.1	32.6	32.6	95.8	95.6	7.6	7.6	4.7	5.3	3	3	-	-	820385	811633	-	-	-	-				
						1.0	-	-	17.3	17.3	8.1	8.1	32.7	95.3	7.5	4.8	3		-		-		-											
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	3.6	-	-	17.3	17.3	8.1	8.1	32.6	84.1	82.8	6.6	5.8	2	-	-	-	-	-	-			-		-		-	-	-	-
						3.6	-	-	17.3	17.3	8.2	8.1	32.6	81.4	82.8	6.4	6.0	2	-	-	-	-	-	-			-		-		-	-	-	-

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 10 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)											
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA								
C1	Cloudy	Moderate	21:04	8.3	Surface	1.0	0.4	207	16.6	16.6	8.2	8.2	32.9	32.9	97.4	97.4	7.8	7.8	2.2	2.4	3	4	46	49	815607	804223	<0.2	<0.2	0.4	0.4										
						1.0	0.4	202	16.6	8.2	8.2	32.9	32.9	97.4	97.4	7.8	2.3		4		46		<0.2				0.4													
					Middle	4.2	0.4	204	16.6	16.6	8.2	8.2	32.9	32.9	97.3	97.4	7.8	2.4	4	48	<0.2	0.4																		
						4.2	0.4	196	16.6	8.2	8.2	32.9	32.9	97.4	97.4	7.8	2.4	3	48	<0.2	0.4																			
					Bottom	7.3	0.3	193	16.6	16.6	8.2	8.2	32.9	32.9	97.5	97.5	7.8	7.8	2.5	5	52	<0.2	0.4																	
						7.3	0.3	193	16.6	8.2	8.2	32.9	32.9	97.5	97.5	7.8	7.8	2.5	6	51	<0.2	0.4																		
						C2	Cloudy	Moderate	19:40	11.6	Surface	1.0	0.3	164	16.4	16.4	8.1	8.1	32.3	32.3	96.2	96.2	7.7	7.8			0.6		0.8		2	2	46	49	825680	806934	<0.2	<0.2	0.6	0.6
												1.0	0.3	170	16.4	8.1	8.1	32.3	32.3	96.2	96.2	7.7	0.6				2				45		<0.2				0.6			
Middle	5.8	0.4	184	16.3	16.3						8.1	8.1	32.3	32.3	96.3	96.3	7.8	0.9	<2	50	<0.2	0.6																		
	5.8	0.4	187	16.3	8.1						8.1	32.3	32.3	96.3	96.3	7.8	0.9	<2	49	<0.2	0.6																			
Bottom	10.6	0.4	160	16.3	16.3						8.2	8.2	32.3	32.3	96.8	96.9	7.8	7.8	0.9	<2	51	<0.2	0.5																	
	10.6	0.4	153	16.3	8.2						8.2	32.3	32.3	96.9	96.9	7.8	7.8	0.9	<2	50	<0.2	0.6																		
	C3	Misty	Calm	20:53	12.0						Surface	1.0	0.3	88	17.5	17.5	8.1	8.1	33.2	33.2	100.5	100.6	7.9	7.9	1.9	2.4	3	2	52	75	822097	817801	<0.2	<0.2			0.4		0.5	
												1.0	0.3	88	17.5	8.1	8.1	33.2	33.2	100.6	100.6	7.9	1.9		2		52		<0.2				0.5							
Middle						6.0	0.3	66	17.5	17.5	8.1	8.1	33.2	33.2	100.8	100.8	7.9	7.9	2.1	85	<0.2	0.5																		
						6.0	0.3	71	17.5	8.1	8.1	33.2	33.2	100.8	100.8	7.9	7.9	2.2	85	<0.2	0.6																			
Bottom						11.0	0.3	77	17.5	17.5	8.1	8.1	33.2	33.2	100.9	101.0	7.9	7.9	3.0	<2	87	<0.2	0.5																	
						11.0	0.3	79	17.5	8.1	8.1	33.2	33.2	101.0	101.0	7.9	7.9	3.0	<2	87	<0.2	0.5																		
						IM1	Cloudy	Moderate	20:44	6.3	Surface	1.0	0.2	190	16.4	16.4	8.2	8.2	32.7	32.7	97.7	97.7	7.9	7.9	3.2	4.2	6	6	47	49			818338		806448	<0.2	<0.2	0.4		0.4
												1.0	0.2	189	16.4	8.2	8.2	32.7	32.7	97.7	97.7	7.9	3.2		5		47		<0.2							0.4				
Middle	3.2	0.3	194	16.3	16.3						8.2	8.2	32.7	32.7	96.9	96.9	7.8	7.8	3.8	48	<0.2	0.4																		
	3.2	0.3	192	16.3	8.2						8.2	32.7	32.7	96.9	96.9	7.8	7.8	3.9	50	<0.2	0.3																			
Bottom	5.3	0.2	199	16.3	16.3						8.2	8.2	32.7	32.7	96.9	96.9	7.8	7.8	5.5	3	52	<0.2	0.4																	
	5.3	0.2	202	16.3	8.2						8.2	32.7	32.7	96.9	96.9	7.8	7.8	5.6	8	51	<0.2	0.4																		
	IM2	Cloudy	Moderate	20:38	6.7						Surface	1.0	0.3	215	16.3	16.3	8.2	8.2	32.7	32.7	97.8	97.8	7.9	7.9	2.4	3.4	6	6	47	49	819168	806239		<0.2		<0.2		0.4	0.4	
												1.0	0.3	221	16.3	8.2	8.2	32.7	32.7	97.8	97.8	7.9	2.4		6		46		<0.2					0.5						
Middle						3.4	0.3	201	16.3	16.3	8.2	8.2	32.7	32.7	97.3	97.3	7.8	7.8	3.6	49	<0.2	0.4																		
						3.4	0.3	207	16.3	8.2	8.2	32.7	32.7	97.3	97.3	7.8	7.8	3.6	5	48	<0.2	0.4																		
Bottom						5.7	0.3	183	16.3	16.3	8.2	8.2	32.7	32.7	97.6	97.7	7.9	7.9	4.0	5	51	<0.2	0.4																	
						5.7	0.3	189	16.3	8.2	8.2	32.7	32.7	97.7	97.7	7.9	7.9	4.2	5	51	<0.2	0.4																		
						IM7	Cloudy	Moderate	20:17	7.4	Surface	1.0	0.2	160	16.3	16.3	8.2	8.2	32.4	32.4	97.5	97.5	7.9	7.9	0.9	1.7	3	3	47	49			821360	806821	<0.2		<0.2	0.5		0.5
												1.0	0.2	155	16.3	8.2	8.2	32.4	32.4	97.5	97.5	7.9	0.9		2		47		<0.2						0.5					
Middle	3.7	0.1	154	16.3	16.3						8.2	8.2	32.6	32.6	97.5	97.6	7.9	7.9	2.0	48	<0.2	0.4																		
	3.7	0.2	159	16.3	8.2						8.2	32.6	32.6	97.7	97.7	7.9	7.9	2.1	49	<0.2	0.4																			
Bottom	6.4	0.1	158	16.3	16.3						8.2	8.2	32.6	32.6	98.1	98.2	7.9	7.9	2.2	2	51	<0.2	0.4																	
	6.4	0.1	157	16.3	8.2						8.2	32.6	32.6	98.2	98.2	7.9	7.9	2.2	3	52	<0.2	0.4																		

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 10 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)						
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	
IM10	Misty	Calm	19:39	8.4	Surface	1.0	0.3	123	17.4	17.4	8.1	8.1	33.1	33.1	100.7	100.7	7.9	7.9	1.1	2.4	2	2	52	77	822237	809843	<0.2	<0.2	0.6	0.5					
						1.0	0.3	130	17.4	8.1	8.1	33.1	33.1	100.7	100.7	7.9	1.1		3		52		<0.2				0.5								
					Middle	4.2	0.3	121	17.3	17.3	8.1	8.1	33.1	33.1	100.7	100.7	7.9	2.6	3	88	<0.2	0.5													
						4.2	0.3	128	17.3	8.1	8.1	33.1	33.1	100.7	100.7	7.9	2.6	2	88	<0.2	0.5														
					Bottom	7.4	0.3	113	17.4	17.4	8.1	8.1	33.1	33.1	101.5	101.5	8.0	8.0	3.6	2	90	<0.2	0.5												
						7.4	0.3	113	17.4	8.1	8.1	33.1	33.1	101.5	101.5	8.0	8.0	3.5	2	90	<0.2	0.6													
IM11	Misty	Calm	19:46	8.2	Surface	1.0	0.4	104	17.3	17.3	8.1	8.1	33.1	33.1	103.1	103.1	8.1	8.1	1.0	2.3	<2	2	63	75	821479	810546	<0.2	<0.2	0.6	0.5					
						1.0	0.4	104	17.3	8.1	8.1	33.1	33.1	103.0	103.0	8.1	1.1		<2		63		<0.2				0.6								
					Middle	4.1	0.4	106	17.3	17.3	8.1	8.1	33.1	33.1	102.4	102.4	8.1	2.2	2	78	<0.2	0.5													
						4.1	0.3	101	17.3	8.1	8.1	33.1	33.1	102.4	102.4	8.1	2.2	2	78	<0.2	0.5														
					Bottom	7.2	0.4	100	17.4	17.4	8.1	8.1	33.0	33.0	105.6	105.8	8.3	8.3	3.6	3	85	<0.2	0.5												
						7.2	0.4	97	17.4	8.1	8.1	33.0	33.0	105.9	105.9	8.3	8.3	3.6	3	85	<0.2	0.5													
IM12	Misty	Calm	19:53	8.6	Surface	1.0	0.4	114	17.4	17.4	8.1	8.1	33.2	33.2	100.7	100.7	7.9	7.9	2.1	3.6	5	4	48	74	821184	811500	<0.2	<0.2	0.6	0.6					
						1.0	0.5	109	17.4	8.1	8.1	33.2	33.2	100.7	100.7	7.9	2.1		4		48		<0.2				0.5								
					Middle	4.3	0.4	107	17.4	17.4	8.1	8.1	33.2	33.2	100.5	100.6	7.9	3.8	4	86	<0.2	0.6													
						4.3	0.4	101	17.4	8.1	8.1	33.2	33.2	100.6	100.6	7.9	3.9	3	86	<0.2	0.5														
					Bottom	7.6	0.4	87	17.4	17.5	8.1	8.1	33.1	33.1	101.8	102.0	8.0	8.0	5.0	3	88	<0.2	0.6												
						7.6	0.4	83	17.5	8.1	8.1	33.1	33.1	102.2	102.2	8.0	8.0	4.9	4	88	<0.2	0.6													
SR1A	Misty	Calm	20:13	5.0	Surface	1.0	0.0	71	17.2	17.2	8.1	8.1	33.0	33.0	101.5	101.6	8.0	8.0	2.7	3.3	3	2	-	-	819971	812661	-	-	-	-					
						1.0	-	70	17.2	8.1	8.1	33.0	33.0	101.6	101.6	8.0	2.7		2		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.0	-	91	17.3	17.3	8.1	8.1	32.9	32.9	102.6	102.8	8.1	8.1	3.9	<2	-	-	-	-			-		-		-	-	-	-	-
						4.0	0.0	94	17.3	8.1	8.1	32.9	32.9	102.9	102.9	8.1	8.1	4.0	<2	-	-	-	-	-			-		-		-	-	-	-	
SR2	Misty	Calm	20:27	5.2	Surface	1.0	0.3	57	17.5	17.5	8.1	8.1	33.0	33.0	101.6	101.7	8.0	8.0	2.1	2.6	<2	4.2	74	83	821472	814189	<0.2	<0.2	0.5	0.5					
						1.0	0.3	56	17.5	8.1	8.1	33.0	33.0	101.8	101.8	8.0	2.2		<2		74		<0.2				0.5								
					Middle	-	0.3	48	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	0.4	41	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
					Bottom	4.2	0.3	47	17.5	17.5	8.1	8.1	32.9	32.8	102.5	104.4	8.1	8.3	3.2	<2	91	<0.2	0.5												
						4.2	0.3	53	17.5	8.1	8.1	32.8	32.8	106.2	106.2	8.4	8.4	3.1	<2	91	<0.2	0.6													
SR3	Cloudy	Moderate	20:10	8.8	Surface	1.0	0.4	156	16.3	16.3	8.2	8.2	32.3	32.3	96.1	96.0	7.8	7.7	1.3	3.8	4	3	-	-	822169	807555	-	-	-	-					
						1.0	0.4	159	16.3	8.2	8.2	32.4	32.4	95.9	95.9	7.7	1.4		3		-		-				-								
					Middle	4.4	0.3	152	16.3	16.3	8.2	8.2	32.5	32.5	95.3	95.3	7.7	4.1	3	-	-	-	-	-			-		-		-	-	-		
						4.4	0.3	157	16.3	8.2	8.2	32.5	32.5	95.3	95.3	7.7	4.1	3	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	7.8	0.3	151	16.3	16.3	8.2	8.2	32.6	32.6	96.0	96.2	7.7	7.8	5.8	<2	-	-	-	-			-		-		-	-	-	-	
						7.8	0.3	152	16.3	8.2	8.2	32.6	32.6	96.4	96.4	7.8	7.8	6.1	<2	-	-	-	-	-			-		-		-	-	-		
SR4A	Cloudy	Moderate	21:25	8.8	Surface	1.0	0.1	339	16.3	16.3	8.2	8.2	32.7	32.7	96.9	96.9	7.8	7.9	4.2	4.5	6	7	-	-	817185	807832	-	-	-	-					
						1.0	0.1	344	16.3	8.2	8.2	32.7	32.7	96.9	96.9	7.8	4.2		7		-		-				-								
					Middle	4.4	0.0	346	16.3	16.3	8.2	8.2	32.7	32.7	97.8	97.9	7.9	4.5	7	-	-	-	-	-			-		-		-	-	-		
						4.4	0.0	352	16.3	8.2	8.2	32.7	32.7	97.9	97.9	7.9	4.6	6	-	-	-	-	-	-			-		-		-	-			
					Bottom	7.8	0.0	346	16.2	16.2	8.2	8.2	32.7	32.7	98.4	98.5	7.9	7.9	4.7	7	-	-	-	-			-		-		-	-	-		
						7.8	0.1	348	16.2	8.2	8.2	32.7	32.7	98.6	98.6	7.9	7.9	4.7	7	-	-	-	-	-			-		-		-	-	-		
SR8	Misty	Calm	19:57	4.8	Surface	1.0	-	-	17.3	17.4	8.1	8.1	33.1	33.1	104.3	104.4	8.2	8.2	3.4	3.9	3	3	-	-	820396	811642	-	-	-	-					
						1.0	-	-	17.4	8.1	8.1	33.1	33.1	104.5	104.5	8.2	3.3		3		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	3.8	-	-	17.4	17.4	8.1	8.1	33.0	33.0	105.8	106.0	8.3	8.3	4.5	3	-	-	-	-			-		-		-	-	-	-	
						3.8	-	-	17.4	8.1	8.1	33.0	33.0	106.1	106.1	8.3	8.3	4.4	2	-	-	-	-	-			-		-		-	-	-		

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 10 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Cloudy	Moderate	08:54	8.4	Surface	1.0	0.1	221	16.6	16.6	8.1	8.1	32.9	32.9	96.9	96.9	7.8		2.0		4		47		815613	804265	<0.2		0.3	
						1.0	0.0	224	16.6		8.1		32.9		96.9		7.7		2.0		4		46				<0.2		0.3	
					Middle	4.2	0.1	197	16.5	16.5	8.2	8.2	32.9	32.9	97.2	97.3	7.8	7.8	3.0	3.2	4	3	47	48			<0.2	<0.2	0.4	0.3
						4.2	0.1	195	16.5		8.2		32.9		97.3		7.9		3.0		3		48				<0.2		0.3	
					Bottom	7.4	0.1	204	16.5	16.5	8.2	8.2	32.9	32.9	98.4	98.5	7.9	7.9	4.5		3		50				<0.2		0.3	
						7.4	0.1	207	16.5		8.2		32.9		98.5		7.9	7.9	5.0		2		51				<0.2		0.3	
					Surface	1.0	0.1	195	16.4	16.4	8.1	8.1	32.3	32.3	95.8	95.9	7.7		0.8		<2		45				<0.2		0.5	
						1.0	0.1	197	16.4		8.1		32.3		95.9		7.7	7.7	0.9		<2		46	48			<0.2		0.5	
C2	Cloudy	Moderate	10:08	11.4	Surface	5.7	0.2	189	16.4	16.4	8.1	8.1	32.3	32.3	96.1	96.1	7.7	7.7	1.3	1.5	<2	<2	47		825678	806948	<0.2	<0.2	0.5	0.6
						5.7	0.2	194	16.4		8.1		32.3		96.1		7.7		1.3		<2		48				<0.2		0.6	
					Middle	10.4	0.1	201	16.3	16.3	8.1	8.1	32.3	32.3	96.5	96.6	7.8	7.8	2.2		<2		51				<0.2		0.6	
						10.4	0.2	202	16.3		8.1		32.3		96.6		7.8		2.4		<2		50				<0.2		0.6	
					Bottom	1.0	0.0	56	17.3	17.3	8.0	8.0	33.2	33.2	100.4	100.6	7.9		2.1		3		44				0.2		0.5	
						1.0	0.0	55	17.3		8.0		33.2		100.7		7.9	7.9	2.2		2		44				0.2		0.5	
					Middle	6.0	0.1	55	17.3	17.3	8.0	7.9	33.2	33.2	101.0	101.1	7.9	7.9	3.3	3.2	3	3	86	72			<0.2	0.2	0.5	0.5
						6.0	0.1	62	17.3		7.9		33.2		101.2		8.0		3.4		2		86				<0.2		0.6	
C3	Misty	Calm	08:24	12.0	Surface	11.0	0.1	73	17.3	17.2	7.9	7.8	33.2	33.1	101.7	107.0	8.0	8.0	4.0		3		86		822127	817784	0.2		0.6	0.5
						11.0	0.1	78	17.0		7.6		33.1		112.2		8.0		4.1		3		87				0.2		0.5	
					Middle	1.0	0.1	189	16.3	16.3	8.2	8.2	32.7	32.7	97.4	97.4	7.8	7.9	2.8	4.0	5	5	47	49			<0.2	<0.2	0.4	0.4
						1.0	0.1	192	16.3		8.2		32.7		97.4		7.8		2.8		6		46				<0.2		0.4	
					Bottom	3.1	0.1	173	16.2	16.2	8.1	8.1	32.7	32.7	97.6	97.7	7.9	7.9	4.0		5		48				<0.2		0.4	
						3.1	0.2	177	16.2		8.1		32.7		97.7		7.9		4.1		6		48				<0.2		0.4	
					Surface	5.1	0.1	186	16.2	16.2	8.1	8.1	32.7	32.7	98.7	98.8	8.0	8.0	5.1		4		51				<0.2		0.4	
						5.1	0.1	187	16.2		8.1		32.7		98.8		8.0		5.5		5		51				<0.2		0.4	
IM2	Cloudy	Moderate	09:20	6.6	Surface	1.0	0.2	202	16.3	16.3	8.2	8.2	32.6	32.6	97.0	97.0	7.8	7.8	2.3	3.5	5	5	46	49	819164	806236	<0.2		0.4	
						1.0	0.2	199	16.3		8.2		32.6		97.0		7.8	7.8	2.3		4		47				<0.2		0.4	
					Middle	3.3	0.2	225	16.3	16.3	8.2	8.2	32.7	32.7	96.6	96.6	7.8	7.8	3.2		5		48				<0.2	<0.2	0.4	0.4
						3.3	0.2	219	16.3		8.2		32.7		96.6		7.8		3.2		4		47				<0.2		0.4	
					Bottom	5.6	0.2	224	16.3	16.3	8.1	8.1	32.7	32.7	96.7	96.7	7.8	7.8	4.9		5		52				<0.2		0.4	
						5.6	0.2	229	16.3		8.2		32.7		96.7		7.8	7.8	5.0		6		51				<0.2		0.4	
					Surface	1.0	0.2	233	16.2	16.2	8.1	8.1	32.3	32.3	96.9	96.9	7.8	7.8	0.9	1.9	3	3	46	48			<0.2	<0.2	0.5	0.5
						1.0	0.2	240	16.2		8.1		32.3		96.9		7.8		0.9		2		47				<0.2		0.5	
IM7	Cloudy	Moderate	09:41	7.6	Middle	3.8	0.1	212	16.2	16.2	8.1	8.1	32.6	32.6	97.0	97.1	7.8	7.8	2.0	1.9	2	3	47	48	821358	806847	<0.2	<0.2	0.5	0.5
						3.8	0.1	208	16.2		8.1		32.6		97.1		7.8		2.0		3		48				<0.2		0.5	
					Bottom	6.6	0.1	209	16.2	16.2	8.1	8.1	32.7	32.7	98.2	98.3	7.9	7.9	3.0		3		51				<0.2		0.5	
						6.6	0.1	211	16.2		8.1		32.7		98.3		7.9	7.9	3.0		3		51				<0.2		0.5	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 10 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)						
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA			
IM10	Misty	Calm	09:36	7.4	Surface	1.0	0.1	134	16.9	16.9	8.1	8.1	33.1	33.1	102.7	102.7	8.2	8.1	1.2	2.6	3	3	48	75	822232	809850	<0.2	0.2	0.5	0.5					
						1.0	0.1	133	16.9	8.1	8.1	33.1	33.1	102.6	102.6	8.1	1.3		4		49		<0.2				0.5								
					Middle	3.7	0.1	149	16.9	16.9	8.1	8.1	33.1	33.1	102.5	102.6	8.1	2.7	2	86	<0.2	0.5													
						3.7	0.1	148	16.9	16.9	8.1	8.1	33.1	33.1	102.6	102.6	8.1	2.6	3	86	<0.2	0.6													
					Bottom	6.4	0.1	121	16.8	16.8	8.1	8.1	33.2	33.2	102.6	102.7	8.2	8.2	4.0	2	89	0.2	0.5												
						6.4	0.1	116	16.8	16.8	8.1	8.1	33.2	33.2	102.7	102.7	8.2	8.2	4.0	3	89	0.2	0.6												
IM11	Misty	Calm	09:29	7.6	Surface	1.0	0.1	140	17.2	17.2	8.1	8.1	33.1	33.1	101.5	101.5	8.0	8.1	2.1	3.3	2	2	52	77	821512	810535	<0.2	<0.2	0.5	0.5					
						1.0	0.1	144	17.2	17.2	8.1	8.1	33.1	33.1	101.5	101.5	8.0		2.2		2		53				<0.2		0.4						
					Middle	3.8	0.0	137	17.2	17.2	8.1	8.1	33.0	33.0	102.0	102.1	8.1	3.3	2	87	<0.2	0.5													
						3.8	0.0	140	17.2	17.2	8.1	8.1	33.1	33.0	102.1	102.1	8.1	3.3	3	87	<0.2	0.5													
					Bottom	6.6	0.1	108	17.0	17.0	8.1	8.1	33.2	33.2	102.5	102.5	8.1	8.1	4.4	2	90	<0.2	0.4												
						6.6	0.0	107	16.9	17.0	8.1	8.1	33.2	33.2	102.5	102.5	8.1	8.1	4.3	2	90	<0.2	0.5												
IM12	Misty	Calm	09:22	8.4	Surface	1.0	0.1	98	17.3	17.3	8.1	8.1	33.1	33.1	99.3	99.3	7.8	7.8	3.4	4.3	3	3	46	73	821166	811499	0.2	0.2	0.5	0.6					
						1.0	0.1	91	17.3	17.3	8.1	8.1	33.1	33.1	99.3	99.3	7.8		3.4		2		45				0.2		0.6						
					Middle	4.2	0.1	113	17.3	17.3	8.1	8.1	33.1	33.1	99.0	99.0	7.8	4.5	3	86	0.2	0.6													
						4.2	0.1	113	17.3	17.3	8.1	8.1	33.1	33.1	98.9	99.0	7.8	4.4	2	86	0.2	0.6													
					Bottom	7.4	0.1	121	17.3	17.3	8.1	8.1	33.0	33.0	99.3	99.4	7.8	7.8	5.0	2	87	<0.2	0.5												
						7.4	0.1	115	17.3	17.3	8.1	8.1	33.0	33.0	99.5	99.5	7.8	7.8	5.1	3	87	<0.2	0.6												
SR1A	Misty	Calm	08:59	5.0	Surface	1.0	0.0	150	17.1	17.1	8.1	8.1	33.0	33.0	100.4	100.5	7.9	8.0	1.9	2.4	2	2	-	-	819981	812659	-	-	-	-					
						1.0	0.0	149	17.1	17.1	8.1	8.1	33.0	33.0	100.6	100.6	8.0		1.9		2		-				-		-						
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
					Bottom	4.0	0.0	150	17.1	17.1	8.1	8.1	33.1	33.1	101.4	101.5	8.0	8.0	2.9	2	-	-	-				-		-		-	-	-	-	-
						4.0	0.0	152	17.0	17.1	8.1	8.1	33.1	33.1	101.5	101.5	8.0	8.0	2.9	3	-	-	-				-		-		-	-	-	-	-
SR2	Misty	Calm	08:45	5.0	Surface	1.0	0.1	34	17.4	17.4	8.0	8.0	33.1	33.1	98.6	98.7	7.8	7.8	3.1	3.6	<2	2	44	65	821484	814180	<0.2	<0.2	0.5	0.5					
						1.0	0.1	40	17.4	17.4	8.0	8.0	33.1	33.1	98.7	98.7	7.8		3.2		<2		43				<0.2		0.4						
					Middle	-	0.1	15	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
						-	0.1	12	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
					Bottom	4.0	0.1	14	17.4	17.4	8.0	8.0	33.1	33.1	98.9	98.9	7.8	7.8	4.0	3	87	<0.2	0.5												
						4.0	0.1	10	17.4	17.4	8.0	8.0	33.1	33.1	98.9	98.9	7.8	7.8	4.1	2	87	<0.2	0.5												
SR3	Cloudy	Moderate	09:48	8.7	Surface	1.0	0.2	160	16.2	16.2	8.1	8.1	32.3	32.3	97.1	97.1	7.8	7.8	1.2	1.9	2	3	-	-	822132	807562	-	-	-	-					
						1.0	0.2	161	16.2	16.2	8.1	8.1	32.3	32.3	97.0	97.0	7.8		1.2		3		-				-								
					Middle	4.4	0.2	179	16.2	16.2	8.1	8.1	32.4	32.4	95.1	95.1	7.7	7.7	1.7	3	-	-	-				-		-		-	-	-		
						4.4	0.2	186	16.2	16.2	8.1	8.1	32.4	32.4	95.0	95.0	7.7	7.7	1.8	4	-	-	-				-		-		-	-	-		
					Bottom	7.7	0.2	148	16.3	16.3	8.1	8.1	32.5	32.5	97.6	97.7	7.9	7.9	2.7	3	-	-	-				-		-		-	-	-	-	
						7.7	0.3	145	16.3	16.3	8.1	8.1	32.5	32.5	97.8	97.7	7.9	7.9	2.7	4	-	-	-				-		-		-	-	-	-	
SR4A	Cloudy	Moderate	08:34	8.2	Surface	1.0	0.0	291	16.3	16.3	8.1	8.1	32.7	32.7	95.9	95.9	7.7	7.7	10.9	7.2	8	8	-	-	817185	807824	-	-	-	-					
						1.0	0.1	289	16.3	16.3	8.1	8.1	32.7	32.7	95.9	95.9	7.7		11.0		7		-				-								
					Middle	4.1	-	286	16.2	16.2	8.1	8.1	32.7	32.7	95.6	95.6	7.7	7.7	5.3	9	-	-	-				-		-		-	-	-		
						4.1	-	283	16.2	16.2	8.1	8.1	32.7	32.7	95.6	95.6	7.7	7.7	5.2	8	-	-	-				-		-		-	-	-		
					Bottom	7.2	0.0	291	16.2	16.2	8.0	8.0	32.7	32.7	95.7	95.8	7.7	7.7	5.3	9	-	-	-				-		-		-	-	-	-	
						7.2	0.0	291	16.2	16.2	8.0	8.0	32.7	32.7	95.8	95.8	7.7	7.7	5.3	9	-	-	-				-		-		-	-	-	-	
SR8	Misty	Calm	09:17	5.0	Surface	1.0	-	-	17.2	17.2	8.1	8.1	33.1	33.1	102.6	102.6	8.1	8.1	3.8	3.9	2	4	-	-	820368	811603	-	-	-	-					
						1.0	-	-	17.1	17.1	8.1	8.1	33.1	33.1	102.6	102.6	8.1		3.8		3		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	
					Bottom	4.0	-	-	17.0	17.0	8.1	8.1	33.3	33.3	102.8	102.8	8.1	8.1	4.1	5	-	-	-				-		-		-	-	-	-	-
						4.0	-	-	16.9	17.0	8.1	8.1	33.3	33.3	102.8	102.8	8.1	8.1	4.1	5	-	-	-				-		-		-	-	-	-	-

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined: **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 12 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Fine	Rough	22:55	7.9	Surface	1.0	0.5	217	18.8	18.8	8.2	8.2	31.1	31.1	106.0	106.1	8.2	8.2	3.5	4.4	<2	<2	82	86	815640	804239	<0.2	<0.2	0.8	0.9
						1.0	0.5	215	18.8	8.2	31.1	106.1	8.2	3.4	<2	82	<0.2		0.8											
					Middle	4.0	0.5	197	18.0	18.0	8.3	8.3	32.0	32.0	104.7	104.7	8.2	3.8	<2	86	<0.2	0.8								
						4.0	0.5	203	18.0	8.3	8.3	32.0	32.0	104.7	104.7	8.2	3.8	<2	87	<0.2	0.7									
					Bottom	6.9	0.5	215	17.9		8.3	8.3	32.8	32.8	101.6	101.6	7.9	7.9	5.8	<2	90	<0.2	1.2							
						6.9	0.5	221	17.9	17.9	8.3	8.3	32.8	32.8	101.6	101.6	7.9	7.9	5.9	<2	90	<0.2	1.2							
C2	Fine	Rough	21:30	10.4	Surface	1.0	0.5	173	18.3	18.3	8.2	8.2	28.0	28.0	104.5	104.5	8.3	8.2	3.3	3.6	<2	<2	82	86	825688	806957	<0.2	<0.2	1.7	1.8
						1.0	0.4	169	18.3	8.2	28.0	104.5	8.3	3.3	<2	83	<0.2		1.8											
					Middle	5.2	0.4	188	17.9	17.9	8.2	8.2	30.5	30.5	102.1	102.1	8.1	8.1	3.4	<2	86	<0.2	1.8							
						5.2	0.4	188	17.9	8.2	30.5	102.1	8.1	3.4	<2	86	<0.2	1.7												
					Bottom	9.4	0.4	152	17.7	17.7	8.2	8.2	32.4	32.4	96.4	96.4	7.6	7.6	4.3	<2	91	<0.2	1.8							
						9.4	0.4	156	17.7	8.2	8.2	32.4	32.4	96.3	96.4	7.6	7.6	4.3	<2	91	<0.2	1.8								
C3	Cloudy	Moderate	22:56	11.7	Surface	1.0	0.4	82	17.5	17.5	8.2	8.2	32.4	32.4	93.1	93.0	7.3	7.3	3.8	3.7	4	3	47	49	822107	817802	<0.2	<0.2	2.0	1.9
						1.0	0.3	82	17.4	8.2	8.2	32.5	32.4	92.8	93.0	7.3	3.8		3		46		<0.2				2.1			
					Middle	5.9	0.4	70	17.2	17.2	8.2	8.2	32.5	32.5	90.8	90.8	7.2	7.2	3.7	3	49	<0.2	2.0							
						5.9	0.4	63	17.2	8.2	32.5	90.8	7.2	3.7	4	49	<0.2	2.1												
					Bottom	10.7	0.3	47	17.2	17.2	8.2	8.2	32.6	32.6	92.8	92.9	7.3	7.4	3.8	3	51	<0.2	1.6							
						10.7	0.3	44	17.1	8.2	32.6	92.9	7.4	3.8	2	52	<0.2	1.5												
IM1	Fine	Rough	22:32	7.8	Surface	1.0	0.4	182	18.1	18.1	8.2	8.2	31.9	31.9	105.8	105.8	8.3	8.3	3.8	4.8	<2	<2	79	87	818328	806470	<0.2	<0.2	0.8	0.8
						1.0	0.4	183	18.1	8.2	31.9	105.7	8.3	3.8	<2	79	<0.2		0.8											
					Middle	3.9	0.4	183	18.1	18.1	8.2	8.2	32.0	32.0	104.9	104.9	8.2	8.2	4.4	<2	87	<0.2	0.9							
						3.9	0.3	190	18.1	8.2	32.0	104.8	8.2	4.4	<2	87	<0.2	0.8												
					Bottom	6.8	0.3	188	17.9		8.3	8.3	32.7	32.7	100.9	100.9	7.9	7.9	6.2	<2	91	<0.2	0.8							
						6.8	0.3	184	17.9	8.3	8.3	32.7	32.7	100.9	100.9	7.9	7.9	6.3	<2	91	<0.2	0.9								
IM2	Fine	Rough	22:26	7.9	Surface	1.0	0.4	197	18.2	18.2	8.3	8.3	31.8	31.9	105.4	105.3	8.2	8.2	3.7	4.0	<2	2	84	88	819170	806222	<0.2	<0.2	0.9	0.8
						1.0	0.4	200	18.1	8.3	31.9	105.2	8.2	3.7	<2	85	<0.2		1.0											
					Middle	4.0	0.4	207	17.9	17.9	8.3	8.3	32.5	32.5	104.5	104.5	8.2	8.2	4.4	2	88	<0.2	0.7							
						4.0	0.4	201	17.9	8.3	32.5	104.4	8.2	4.4	2	88	<0.2	0.7												
					Bottom	6.9	0.3	192	17.9		8.3	8.3	32.6	32.6	104.1	104.1	8.1	8.1	3.9	2	91	<0.2	0.7							
						6.9	0.3	188	17.9	8.3	32.6	104.0	8.1	3.9	2	91	<0.2	0.8												
IM7	Fine	Rough	22:05	8.6	Surface	1.0	0.2	170	18.3	18.3	8.2	8.2	27.8	27.8	103.3	103.3	8.2	8.0	3.3	3.8	<2	2	83	86	821369	806851	<0.2	<0.2	0.9	0.9
						1.0	0.2	163	18.3	8.2	27.8	103.3	8.2	3.3	<2	83	<0.2		0.8											
					Middle	4.3	0.2	171	17.8	17.8	8.2	8.2	32.2	32.1	98.6	98.6	7.7	7.7	4.0	3	86	<0.2	0.8							
						4.3	0.2	175	17.8	8.2	32.1	98.6	7.7	4.0	2	86	<0.2	0.8												
					Bottom	7.6	0.2	181	17.8		8.2	8.2	32.2	32.2	98.1	98.1	7.7	7.7	4.2	3	90	<0.2	0.9							
						7.6	0.3	179	17.8	8.2	32.2	98.1	7.7	4.2	2	90	<0.2	0.9												

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; Value exceeding Limit Level is bolded and underlined
Note: The DCM monitoring was resumed starting from 11 January 2022.

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 12 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)							
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA				
IM10	Cloudy	Moderate	21:25	7.8	Surface	1.0	0.4	100	17.4	17.4	8.2	8.2	27.3	27.3	101.4	101.4	8.3	7.9	3.6	4.0	3	3	46	49	822239	809834	<0.2	<0.2	2.4	2.1						
						1.0	0.4	94	17.4	17.4	8.2	8.2	27.3	27.3	101.3	101.4	8.2		3.6		2		47				<0.2		2.4							
					Middle	3.9	0.4	87	17.1	17.1	8.2	8.2	31.5	31.5	95.1	95.0	7.6	4.1	3	49	<0.2	2.3														
						3.9	0.4	83	17.1	17.1	8.2	8.2	31.6	31.5	94.9	95.0	7.6	4.1	2	48	<0.2	2.3														
					Bottom	6.8	0.4	127	17.1	17.1	8.2	8.2	31.9	31.9	95.2	95.2	7.6	4.4	2	51	<0.2	1.6														
						6.8	0.4	133	17.1		8.2	8.2	31.9		31.9		95.2	7.6	4.2	3	52	<0.2	1.5													
IM11	Cloudy	Moderate	21:54	7.3	Surface	1.0	0.5	94	17.3	17.3	8.3	8.3	28.8	28.8	99.2	99.1	8.0	7.8	4.0	5.0	3	3	48	50	821515	810559	<0.2	<0.2	2.4	2.0						
						1.0	0.5	95	17.3	17.3	8.3	8.3	28.8	28.8	98.9	99.1	8.0		4.1		3		49				<0.2		2.3							
					Middle	3.7	0.5	109	17.2	17.2	8.3	8.3	31.8	31.8	96.1	96.1	7.6	5.4	3	50	<0.2	1.6														
						3.7	0.5	102	17.2	17.2	8.3	8.3	31.8	31.8	96.0	96.1	7.6	5.4	3	48	<0.2	1.6														
					Bottom	6.3	0.6	109	17.2	17.2	8.3	8.3	32.0	32.0	96.2	96.3	7.6	5.4	2	52	<0.2	2.2														
						6.3	0.5	112	17.2	17.2	8.3	8.3	32.0	32.0	96.3	96.3	7.7	5.5	2	53	<0.2	2.1														
IM12	Cloudy	Moderate	22:00	7.8	Surface	1.0	0.5	88	17.4	17.4	8.2	8.2	27.8	27.9	102.2	102.2	8.3	8.0	3.7	3.9	3	3	48	50	821174	811528	<0.2	<0.2	1.7	1.8						
						1.0	0.6	91	17.3	17.4	8.2	8.2	27.9	102.1	102.2	8.3	3.8		4		48		<0.2				1.7									
					Middle	3.9	0.6	89	17.2	17.2	8.2	8.2	31.5	31.6	97.2	97.1	7.7	3.8	2	50	<0.2	1.8														
						3.9	0.6	84	17.2	17.2	8.2	8.2	31.7	31.6	97.0	97.1	7.7	3.8	2	49	<0.2	1.8														
					Bottom	6.8	0.5	92	17.1	17.1	8.2	8.2	32.2	32.1	96.8	96.9	7.7	4.2	2	52	<0.2	1.9														
						6.8	0.5	88	17.1	17.1	8.2	8.2	32.1	32.1	97.0	96.9	7.7	4.2	<2	54	<0.2	2.0														
SR1A	Cloudy	Moderate	22:25	5.2	Surface	1.0	-	101	17.3	17.3	8.2	8.2	31.3	31.3	97.4	97.3	7.8	7.8	4.6	4.7	5	4	-	-	819971	812659	-	-	-	-						
						1.0	0.1	98	17.3	17.3	8.2	8.2	31.4	31.3	97.2	97.3	7.7		4.7		4		-				-		-							
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-		
					Bottom	4.2	0.0	75	17.2	17.2	8.2	8.2	31.8	31.7	97.2	97.3	7.7	4.8	3	-	-	-	-	-			-		-		-	-	-	-	-	
						4.2	0.0	68	17.2	17.2	8.2	8.2	31.7	31.7	97.3	97.3	7.7	4.7	2	-	-	-	-	-			-		-		-	-	-	-	-	
SR2	Cloudy	Moderate	22:37	4.1	Surface	1.0	0.4	33	17.6	17.6	8.2	8.2	29.5	29.6	102.9	102.8	8.2	8.2	3.6	3.7	2	2	49	50	821469	814154	<0.2	<0.2	1.9	1.9						
						1.0	0.4	27	17.6	17.6	8.2	8.2	29.6	102.7	102.7	8.2	3.7		2		48		<0.2				1.9									
					Middle	-	0.4	50	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	-	
						-	0.5	50	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	-	
					Bottom	3.1	0.4	58	17.5	17.5	8.2	8.2	30.3	30.3	101.1	101.0	8.1	8.1	3.8	3	51	<0.2	1.9													
						3.1	0.5	52	17.5	17.5	8.2	8.2	30.4	30.3	100.8	101.0	8.0	3.8	2	52	<0.2	2.0														
SR3	Fine	Rough	21:59	9.5	Surface	1.0	0.4	169	18.2	18.2	8.2	8.2	27.3	27.2	103.1	103.1	8.3	8.0	3.4	3.9	<2	4.2	-	-	822140	807589	-	-	-	-						
						1.0	0.5	166	18.2	18.2	8.2	8.2	27.2	103.1	103.1	8.3	3.4		<2		-		-				-									
					Middle	4.8	0.4	165	17.8	17.8	8.2	8.2	31.7	31.7	97.8	97.8	7.7	3.9	<2	-	-	-	-	-			-		-		-	-	-	-		
						4.8	0.4	162	17.8	17.8	8.2	8.2	31.7	31.7	97.8	97.8	7.7	3.9	<2	-	-	-	-	-			-		-		-	-	-	-		
					Bottom	8.5	0.5	142	17.7	17.7	8.2	8.2	32.0	32.0	96.0	96.0	7.6	4.5	<2	-	-	-	-	-			-		-		-	-	-	-	-	
						8.5	0.4	140	17.7	17.7	8.2	8.2	32.0	32.0	96.0	96.0	7.6	4.4	<2	-	-	-	-	-			-		-		-	-	-	-	-	
SR4A	Fine	Moderate	23:25	9.9	Surface	1.0	0.0	37	18.2	18.2	8.3	8.3	31.8	31.8	104.4	104.4	8.1	8.1	3.8	4.6	<2	4.6	-	-	817176	807816	-	-	-	-						
						1.0	0.0	29	18.2	18.2	8.3	8.3	31.8	31.8	104.4	104.4	8.1		3.8		<2		-				-		-							
					Middle	5.0	0.1	61	18.0	18.0	8.3	8.3	32.1	32.1	102.7	102.7	8.0	4.6	<2	-	-	-	-	-			-		-		-	-	-	-		
						5.0	0.0	55	18.0	18.0	8.3	8.3	32.1	32.1	102.7	102.7	8.0	4.6	<2	-	-	-	-	-			-		-		-	-	-	-		
					Bottom	8.9	0.0	28	17.8	17.8	8.3	8.3	32.4	32.4	100.4	100.4	7.9	5.3	<2	-	-	-	-	-			-		-		-	-	-	-	-	
						8.9	0.1	24	17.8	17.8	8.3	8.3	32.4	32.4	100.4	100.4	7.9	5.3	<2	-	-	-	-	-			-		-		-	-	-	-	-	
SR8	Cloudy	Moderate	22:05	4.7	Surface	1.0	-	-	17.7	17.7	8.3	8.3	30.1	30.2	100.4	100.4	8.0	8.0	4.1	4.3	2	2	-	-	820396	811641	-	-	-	-						
						1.0	-	-	17.7	17.7	8.3	8.3	30.2	30.2	100.4	100.4	8.0		4.1		3		-				-		-							
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	-	
					Bottom	3.7	-	-	17.8	17.8	8.3	8.3	31.0	31.0	100.2	100.2	7.9	4.4	<2	-	-	-	-	-			-		-		-	-	-	-	-	-
						3.7	-	-	17.8	17.8	8.3	8.3	31.0	31.0	100.2	100.2	7.9	4.4	<2	-	-	-	-	-			-		-		-	-	-	-	-	-

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined: **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 12 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)						
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	
C1	Sunny	Rough	11:08	6.9	Surface	1.0	0.0	202	18.1	18.1	8.2	8.2	31.6	31.6	102.8	102.8	8.1	8.0	5.9	7.5	2	3	79	85	815633	804227	<0.2	0.9	0.9						
						1.0	0.0	206	18.1		8.2	8.2	31.6	31.6	102.8	102.8	8.1		5.9		3		79				<0.2	0.9							
					Middle	3.5	0.1	181	17.8	17.8	8.2	8.2	32.8	32.8	100.6	100.6	7.9	7.3	2	86	<0.2	0.9													
						3.5	0.1	181	17.8		8.2	8.2	32.8	32.8	100.6	100.6	7.9	7.3	3	86	<0.2	0.9													
					Bottom	5.9	0.0	191	17.8	17.8	8.2	8.2	32.8	32.8	100.1	100.1	7.8	9.4	3	90	<0.2	0.8													
						5.9	0.0	193	17.8		8.2	8.2	32.8	32.8	100.1	100.1	7.8	9.4	2	90	<0.2	0.9													
					C2	Sunny	Rough	12:21	9.7	Surface	1.0	0.0	342	18.2	18.2	8.2	8.2	27.4	27.4	102.7	102.7	8.2	8.0	5.6	5.9	<2	<2	83		87	825670	806952	<0.2	1.8	1.8
											1.0	0.0	337	18.2		8.2	8.2	27.4	27.4	102.7	102.7	8.2		5.6		83		<0.2					1.8		
Middle	4.9	0.0	332	17.7						17.7	8.2	8.2	31.6	31.6	97.3	97.3	7.7	6.2	<2	86	<0.2	1.8													
	4.9	0.0	328	17.7							8.2	8.2	31.6	31.6	97.3	97.3	7.7	6.3	<2	86	<0.2	1.8													
Bottom	8.7	0.0	318	17.6						17.6	8.2	8.2	32.2	32.2	96.9	96.9	7.6	5.8	<2	91	<0.2	1.8													
	8.7	0.0	322	17.6							8.2	8.2	32.2	32.2	96.9	96.9	7.6	5.8	<2	91	<0.2	1.9													
C3	Cloudy	Moderate	10:04	11.6						Surface	1.0	0.0	237	17.2	17.2	8.1	8.1	32.6	32.6	89.1	89.1	7.1	7.1	4.0	5.4	2	3	47	50	822110	817805	<0.2	2.4	2.2	
											1.0	0.0	233	17.2		8.1	8.1	32.6	32.6	89.0	89.1	7.1		4.1		3		48				<0.2	2.6		
					Middle	5.8	0.0	213	17.1	17.1	8.1	8.1	32.6	32.6	88.6	88.6	7.0	4.6	2	50	<0.2	1.9													
						5.8	0.0	216	17.1		8.1	8.1	32.6	32.6	88.5	88.6	7.0	4.7	3	49	<0.2	1.9													
					Bottom	10.6	0.0	226	17.1	17.1	8.1	8.1	32.6	32.6	88.4	88.4	7.0	7.1	3	52	<0.2	2.2													
						10.6	0.0	229	17.1		8.1	8.1	32.6	32.6	88.4	88.4	7.0	8.1	4	52	<0.2	2.0													
					IM1	Sunny	Moderate	11:23	6.7	Surface	1.0	0.0	142	18.1	18.1	8.2	8.2	31.7	31.7	103.2	103.2	8.1	8.1	5.8	6.1	2	3	82	86	818354	806439	<0.2	0.9		0.9
											1.0	0.1	144	18.1		8.2	8.2	31.7	31.7	103.2	103.2	8.1		5.8		3		82				<0.2	0.9		
Middle	3.4	0.0	141	17.9						17.9	8.2	8.2	32.0	32.0	102.6	102.6	8.0	6.1	6	87	<0.2	0.9													
	3.4	-	140	17.9							8.2	8.2	32.0	32.0	102.6	102.6	8.0	6.1	2	87	<0.2	0.9													
Bottom	5.7	0.0	164	17.8						17.8	8.2	8.2	32.5	32.5	100.7	100.7	7.9	6.4	2	90	<0.2	0.7													
	5.7	0.1	164	17.8							8.2	8.2	32.5	32.5	100.7	100.7	7.9	6.5	2	90	<0.2	0.8													
IM2	Sunny	Moderate	11:29	8.4						Surface	1.0	0.1	210	18.1	18.1	8.2	8.2	31.7	31.7	102.5	102.5	8.0	8.0	5.8	7.0	<2	2	79	83	819177	806216	<0.2	1.9	1.9	
											1.0	0.1	217	18.1		8.2	8.2	31.7	31.7	102.5	102.5	8.0		5.8		<2		79				<0.2	1.9		
					Middle	4.2	0.1	178	17.8	17.8	8.3	8.3	32.6	32.6	101.0	101.0	7.9	6.2	2	83	<0.2	1.8													
						4.2	0.1	175	17.8		8.3	8.3	32.6	32.6	101.0	101.0	7.9	6.2	2	83	<0.2	1.9													
					Bottom	7.4	0.0	174	17.7	17.7	8.3	8.3	32.9	32.9	99.1	99.2	7.8	8.9	2	87	<0.2	2.0													
						7.4	0.0	172	17.7		8.3	8.3	32.9	32.9	99.2	99.2	7.8	8.9	2	87	<0.2	2.0													
					IM7	Sunny	Rough	11:51	8.7	Surface	1.0	0.0	104	18.3	18.3	8.2	8.2	27.8	27.8	102.1	102.1	8.1	7.9	5.3	5.7	2	2	82	87	821356	806824	<0.2	1.8		1.8
											1.0	0.1	102	18.3		8.2	8.2	27.8	27.8	102.1	102.1	8.1		5.3		2		82				<0.2	1.7		
Middle	4.4	0.0	122	17.8						17.8	8.2	8.2	32.1	32.1	98.0	98.0	7.7	5.6	2	86	<0.2	2.0													
	4.4	0.0	129	17.8							8.2	8.2	32.1	32.1	98.0	98.0	7.7	5.7	2	87	<0.2	1.9													
Bottom	7.7	0.0	115	17.8						17.9	8.3	8.3	32.2	32.2	97.5	97.5	7.6	6.2	2	91	<0.2	1.7													
	7.7	0.0	119	17.9							8.3	8.3	32.2	32.2	97.5	97.5	7.6	6.2	3	91	<0.2	1.8													

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 12 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)							
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA				
IM10	Cloudy	Moderate	11:43	7.5	Surface	1.0	0.0	119	17.4	17.4	8.2	8.2	27.3	27.3	100.3	100.1	8.2	7.9	3.6	4.2	<2	2	48	50	822243	809846	<0.2	<0.2	1.6	2.0						
						1.0	0.0	116	17.4	8.2	8.2	27.3	99.9	8.1	3.7	<2	48		<0.2		1.8															
					Middle	3.8	0.0	98	17.1	17.1	8.2	8.2	31.1	31.1	96.7	96.7	7.7	4.1	2	50	<0.2	2.1														
						3.8	0.0	101	17.1	8.2	8.2	31.1	96.6	7.7	4.1	2	49	<0.2	2.2																	
					Bottom	6.5	0.0	126	17.1	8.2	8.2	32.0	95.5	95.6	7.6	7.6	4.6	2	52	<0.2	2.2															
						6.5	0.0	123	17.1	8.2	8.2	32.0	95.6	7.6	7.6	5.0	2	53	<0.2	2.2																
IM11	Cloudy	Moderate	11:35	7.8	Surface	1.0	0.0	147	17.4	17.4	8.2	8.2	28.1	28.1	100.8	100.8	8.2	8.0	3.8	5.2	<2	2	47	49	821481	810528	<0.2	<0.2	2.5	2.3						
						1.0	0.0	154	17.4	8.2	8.2	28.1	100.7	8.2	3.8	<2	48		<0.2		2.6															
					Middle	3.9	0.1	116	17.2	17.2	8.2	8.2	31.2	31.2	97.9	97.9	7.8	5.9	3	49	<0.2	2.2														
						3.9	0.1	117	17.2	8.2	8.2	31.3	97.8	7.8	6.3	2	48	<0.2	2.2																	
					Bottom	6.8	0.1	114	17.2	17.2	8.2	8.2	32.1	32.1	95.9	96.0	7.6	5.7	3	52	<0.2	2.2														
						6.8	0.1	109	17.2	8.2	8.2	32.1	96.0	7.6	7.6	5.8	2	52	<0.2	2.1																
IM12	Cloudy	Moderate	11:26	8.2	Surface	1.0	0.0	109	17.4	17.4	8.2	8.2	28.5	28.5	101.2	101.2	8.2	8.0	3.7	4.0	<2	2	46	48	821171	811540	<0.2	<0.2	2.7	2.4						
						1.0	0.0	110	17.4	8.2	8.2	28.5	101.2	8.2	3.7	<2	47		<0.2		2.7															
					Middle	4.1	0.1	110	17.2	17.2	8.2	8.2	31.9	31.9	97.1	97.0	7.7	4.0	<2	48	<0.2	2.4														
						4.1	0.1	108	17.1	8.2	8.2	31.9	96.8	7.7	4.0	<2	47	<0.2	2.4																	
					Bottom	7.2	0.1	138	17.1	17.1	8.2	8.2	32.2	32.2	95.5	95.5	7.6	4.4	2	51	<0.2	2.0														
						7.2	0.0	135	17.1	8.2	8.2	32.2	95.5	7.6	7.6	4.4	2	51	<0.2	2.0																
SR1A	Cloudy	Moderate	10:47	5.1	Surface	1.0	0.0	174	17.1	17.1	8.2	8.2	31.2	31.3	96.1	96.1	7.7	7.7	4.5	4.7	3	3	-	-	819973	812661	-	-	-	-						
						1.0	0.0	167	17.1	8.2	8.2	31.4	96.0	7.7	4.5	2	-		-		-															
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-				-		-		-	-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-				-		-		-	-	-	-	-	
					Bottom	4.1	0.0	158	17.1	17.1	8.2	8.2	32.0	32.0	96.0	96.1	7.6	5.0	2	-	-		-				-		-		-	-	-	-	-	-
						4.1	-	162	17.1	8.2	8.2	32.0	96.1	7.6	7.6	4.9	3	-	-	-	-		-				-		-		-	-	-	-	-	-
SR2	Cloudy	Moderate	10:26	3.7	Surface	1.0	0.1	9	17.1	17.1	8.1	8.1	31.5	31.6	98.4	98.4	7.8	7.8	3.6	3.7	<2	2	48	50	821477	814172	<0.2	<0.2	2.6	2.3						
						1.0	0.1	13	17.1	8.1	8.1	31.6	98.3	7.8	3.6	<2	49		<0.2		2.4															
					Middle	-	0.1	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	-	
						-	-	356	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-				-		-		-	-	-	-	-	
					Bottom	2.7	0.1	6	17.1	17.1	8.1	8.1	31.8	31.8	98.3	98.3	7.8	3.7	2	51	<0.2	2.1														
						2.7	0.1	5	17.1	8.1	8.1	31.8	98.3	7.8	7.8	3.7	3	50	<0.2	2.1																
SR3	Sunny	Rough	11:57	8.9	Surface	1.0	0.1	177	18.2	18.2	8.2	8.2	27.2	27.2	102.4	102.4	8.2	8.0	5.3	6.1	<2	2	-	-	822164	807577	-	-	-	-						
						1.0	0.1	180	18.2	8.2	8.2	27.2	102.4	8.2	5.3	<2	-		-		-															
					Middle	4.5	0.1	180	17.8	17.8	8.2	8.2	31.6	31.6	97.5	97.5	7.7	5.9	2	-	-	-	-				-		-		-	-	-	-		
						4.5	0.0	180	17.8	8.2	8.2	31.6	97.4	7.7	5.9	3	-	-	-	-	-	-	-				-		-		-	-	-			
					Bottom	7.9	0.0	183	17.7	17.7	8.2	8.2	32.0	32.0	97.1	97.2	7.6	7.2	2	-	-	-	-				-		-		-	-	-	-		
						7.9	0.0	182	17.7	8.2	8.2	32.0	97.2	7.6	7.6	7.2	3	-	-	-	-	-	-				-		-		-	-	-	-		
SR4A	Sunny	Moderate	10:39	9.8	Surface	1.0	0.0	291	17.9	17.9	8.2	8.2	31.7	31.7	102.3	102.3	8.0	8.0	5.9	6.6	2	4	-	-	817188	807799	-	-	-	-						
						1.0	0.1	286	17.9	8.2	8.2	31.7	102.3	8.0	5.9	2	-		-		-															
					Middle	4.9	0.0	298	17.8	17.8	8.2	8.2	32.2	32.2	100.2	100.2	7.9	6.6	4	-	-		-				-		-		-	-	-	-	-	
						4.9	0.0	301	17.8	8.2	8.2	32.2	100.2	7.9	6.6	5	-	-	-	-	-		-				-		-		-	-	-	-		
					Bottom	8.8	0.0	288	17.8	17.8	8.2	8.2	32.5	32.5	98.9	98.9	7.7	7.5	4	-	-		-				-		-		-	-	-	-	-	
						8.8	0.0	283	17.8	8.2	8.2	32.5	98.9	7.7	7.7	7.5	5	-	-	-	-		-				-		-		-	-	-	-	-	
SR8	Cloudy	Moderate	11:09	4.7	Surface	1.0	-	-	17.3	17.3	8.3	8.3	31.3	31.4	97.9	97.8	7.8	7.8	7.9	9.3	2	3	-	-	820381	811628	-	-	-	-						
						1.0	-	-	17.3	8.3	8.3	31.4	97.7	7.8	8.6	3	-		-		-															
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-				-		-		-	-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-				-		-		-	-	-	-	-	
					Bottom	3.7	-	-	17.2	17.2	8.3	8.3	32.1	32.1	96.5	96.4	7.7	10.4	3	-	-		-				-		-		-	-	-	-	-	-
						3.7	-	-	17.2	8.3	8.3	32.1	96.2	7.6	7.7	10.6	2	-	-	-	-		-				-		-		-	-	-	-	-	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined: **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 15 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Cloudy	Moderate	12:17	8.3	Surface	1.0	0.1	189	18.2	18.2	8.3	8.3	32.3	32.3	102.5	102.5	8.0	7.9	2.2		2		47	49	815602	804227	0.3		0.5	
						1.0	0.1	182	18.2	18.2	8.3	8.3	32.3	32.3	102.4	102.5	8.0	7.9	2.3		3		47	49			0.3		0.5	
					Middle	4.2	0.1	163	18.0	18.0	8.3	8.3	32.9	32.9	100.3	100.3	7.8	7.7	4.7	5.3	4	4	50	49			0.3	0.3	0.5	0.5
						4.2	0.0	165	18.0	18.0	8.3	8.3	32.9	32.9	100.3	100.3	7.8	7.7	4.8	5.3	5	4	49	51			0.3		0.5	
					Bottom	7.3	0.0	177	18.0	18.0	8.2	8.2	32.9	32.9	99.0	99.0	7.7	7.7	8.9		4		51	52			0.3		0.5	
						7.3	0.0	179	18.0	18.0	8.2	8.2	32.9	32.9	99.0	99.0	7.7	7.7	8.9		4		51	52			0.3		0.5	
						1.0	0.1	17	18.0	18.0	8.2	8.2	30.5	30.5	97.4	97.4	7.7	7.7	1.2		<2		46	49			0.3		0.9	
						1.0	0.1	18	18.0	18.0	8.2	8.2	30.5	30.5	97.4	97.4	7.7	7.7	1.2		<2		47	49			0.3		0.9	
C2	Cloudy	Moderate	10:58	12.1	Surface	6.1	0.1	14	18.0	18.0	8.2	8.2	30.8	30.8	98.0	98.0	7.7	7.7	1.6	3.0	2	2	48	49	825678	806926	0.3		0.8	
						6.1	0.1	13	18.0	18.0	8.2	8.2	30.8	30.8	98.0	98.0	7.7	7.7	1.7	3.0	2	2	49	51			0.2	0.3	0.9	0.9
					Bottom	11.1	0.1	341	18.1	18.1	8.2	8.2	31.5	31.5	97.8	97.8	7.7	7.7	6.1		2		51	51			0.2		0.9	
						11.1	0.1	347	18.1	18.1	8.2	8.2	31.5	31.5	97.8	97.8	7.7	7.7	6.0		3		51	51			0.3		0.9	
					Surface	1.0	0.1	89	17.5	17.5	8.3	8.3	30.9	30.9	98.8	98.8	7.8	7.9	4.1		<2		52	74	822112	817821	0.3		0.8	
						1.0	0.1	92	17.5	17.5	8.3	8.3	30.9	30.9	98.8	98.8	7.9	7.9	4.2		<2		52	74			0.2		0.8	
					Middle	6.0	0.2	86	17.5	17.5	8.3	8.3	30.9	30.9	99.0	99.0	7.9	7.9	5.6	5.2	4	3	82	87			0.3	0.3	0.9	0.8
						6.0	0.2	84	17.5	17.5	8.3	8.3	30.9	30.9	99.0	99.0	7.9	7.9	5.5	5.2	3	3	82	87			0.3		0.8	
C3	Misty	Calm	12:01	12.0	Surface	11.0	0.1	104	17.6	17.6	8.3	8.3	30.9	30.9	99.1	99.1	7.9	7.9	6.0		4		87	87	822112	817821	0.2		0.8	
						11.0	0.1	101	17.6	17.6	8.3	8.3	30.9	30.9	99.1	99.1	7.9	7.9	6.1		3		87	87			0.2		0.8	
					Bottom	1.0	0.0	98	18.3	18.3	8.3	8.3	31.6	31.6	101.0	101.0	7.9	7.9	2.0		2		45	48			0.2		0.6	
						1.0	0.1	98	18.3	18.3	8.3	8.3	31.6	31.6	101.0	101.0	7.9	7.9	2.0		2		45	48			<0.2		0.6	
					Middle	3.3	0.0	78	18.2	18.2	8.3	8.3	31.7	31.7	100.6	100.5	7.8	7.8	2.3	2.4	3	3	48	48			<0.2	0.2	0.6	0.6
						3.3	-	84	18.2	18.2	8.3	8.3	31.7	31.7	100.3	100.5	7.8	7.8	3.5	2.4	3	3	48	48			<0.2		0.6	
					Bottom	5.6	0.1	71	18.2	18.2	8.3	8.3	31.8	31.8	99.2	99.2	7.7	7.7	2.4		4		50	49			<0.2		0.6	
						5.6	0.0	73	18.2	18.2	8.3	8.3	31.8	31.8	99.2	99.2	7.7	7.7	2.4		5		49	49			<0.2		0.5	
IM1	Cloudy	Moderate	11:58	6.6	Surface	1.0	0.0	39	18.2	18.2	8.2	8.2	31.6	31.6	100.6	100.5	7.9	7.8	2.0		5		45	48	819186	806231	<0.2		0.8	
						1.0	0.0	32	18.2	18.2	8.3	8.2	31.6	31.6	100.4	100.5	7.8	7.8	2.3		4		45	48			<0.2		0.7	
					Middle	3.6	0.1	31	18.2	18.2	8.3	8.3	31.7	31.7	99.5	99.5	7.8	7.8	2.2	4.1	5	4	48	48			<0.2	<0.2	0.8	0.8
						3.6	0.0	30	18.1	18.1	8.3	8.3	31.7	31.7	99.4	99.4	7.8	7.8	2.2	4.1	4	4	48	48			<0.2		0.8	
					Bottom	6.1	0.1	52	18.2	18.2	8.3	8.3	31.9	31.9	98.2	98.1	7.7	7.7	7.9		3		50	50			<0.2		0.7	
						6.1	0.0	48	18.2	18.2	8.3	8.3	31.9	31.9	97.9	98.1	7.6	7.6	8.0		4		50	50			<0.2		0.7	
					Surface	1.0	0.2	51	18.1	18.1	8.2	8.2	30.5	30.5	98.4	98.3	7.8	7.7	0.8		<2		45	48	821368	806828	<0.2		0.8	
						1.0	0.2	55	18.1	18.1	8.2	8.2	30.5	30.5	98.2	98.3	7.7	7.7	0.9		<2		45	48			<0.2		0.8	
IM2	Fine	Moderate	11:50	7.1	Middle	4.4	0.2	54	18.1	18.1	8.2	8.2	31.3	31.3	97.5	97.4	7.6	7.5	1.5	1.3	<2	2	48	48			<0.2	<0.2	0.9	0.9
						4.4	0.2	51	18.1	18.1	8.2	8.2	31.3	31.3	97.3	97.4	7.6	7.5	1.5	1.3	<2	2	49	50			<0.2		0.9	
					Bottom	7.8	0.2	65	18.1	18.1	8.2	8.2	31.4	31.4	96.2	96.3	7.5	7.5	1.4		3		50	50			<0.2		0.9	
						7.8	0.3	62	18.1	18.1	8.2	8.2	31.4	31.4	96.3	96.3	7.5	7.5	1.6		2		50	50			<0.2		0.9	
					Surface	1.0	0.2	51	18.1	18.1	8.2	8.2	30.5	30.5	98.4	98.3	7.8	7.7	0.8		<2		45	48	821368	806828	<0.2		0.8	
						1.0	0.2	55	18.1	18.1	8.2	8.2	30.5	30.5	98.2	98.3	7.7	7.7	0.9		<2		45	48			<0.2		0.8	
					Middle	4.4	0.2	54	18.1	18.1	8.2	8.2	31.3	31.3	97.5	97.4	7.6	7.5	1.5	1.3	<2	2	48	48			<0.2	<0.2	0.9	0.9
						4.4	0.2	51	18.1	18.1	8.2	8.2	31.3	31.3	97.3	97.4	7.6	7.5	1.5	1.3	<2	2	49	50			<0.2		0.9	
IM7	Fine	Moderate	11:29	8.8	Bottom	7.8	0.2	65	18.1	18.1	8.2	8.2	31.4	31.4	96.2	96.3	7.5	7.5	1.4		3		50	50			<0.2		0.9	
						7.8	0.3	62	18.1	18.1	8.2	8.2	31.4	31.4	96.3	96.3	7.5	7.5	1.6		2		50	50			<0.2		0.9	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 15 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)						
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	
IM10	Misty	Calm	10:57	8.4	Surface	1.0	0.0	353	17.3	17.3	8.3	8.3	30.5	30.5	98.0	98.1	7.8	7.9	1.8	2.4	3	3	52	77	822232	809845	<0.2	<0.2	0.7	0.7					
						1.0	0.0	357	17.3	8.3	8.3	30.5	30.5	98.1	98.5	7.8	1.8		3		52		<0.2				0.7								
					Middle	4.2	0.1	13	17.3	17.3	8.3	8.3	30.6	30.6	98.5	98.5	7.9	2.2	3	87	<0.2	0.7													
						4.2	0.1	13	17.3	8.3	8.3	30.6	30.6	98.5	98.5	7.9	2.2	2	88	<0.2	0.7														
					Bottom	7.4	0.0	12	17.3	17.3	8.3	8.3	30.6	30.6	99.3	99.4	7.9	7.9	3.1	90	<0.2	0.7													
						7.4	0.0	6	17.3	8.3	8.3	30.6	30.6	99.4	99.4	7.9	7.9	3.1	90	<0.2	0.7														
IM11	Misty	Calm	11:01	8.2	Surface	1.0	0.1	301	17.4	17.4	8.3	8.3	30.8	30.8	98.4	98.4	7.8	7.8	1.0	1.5	2	3	63	75	821505	810542	<0.2	<0.2	0.9	0.9					
						1.0	0.1	298	17.3	8.3	8.3	30.9	30.9	98.4	98.4	7.8	1.1		2		63		<0.2				0.9								
					Middle	4.1	0.1	315	17.4	17.4	8.3	8.3	30.9	30.9	98.4	98.4	7.8	1.2	2	78	<0.2	0.9													
						4.1	0.1	312	17.4	8.3	8.3	30.9	30.9	98.4	98.4	7.8	1.2	3	79	<0.2	1.0														
					Bottom	7.2	0.1	309	17.5	17.5	8.3	8.3	30.8	30.8	99.0	99.0	7.9	7.9	2.1	85	<0.2	0.7													
						7.2	0.1	311	17.5	8.3	8.3	30.8	30.8	99.0	99.0	7.9	7.9	2.2	3	84	<0.2	0.7													
IM12	Misty	Calm	11:10	8.6	Surface	1.0	0.1	14	17.3	17.3	8.3	8.3	30.9	30.9	97.9	97.9	7.8	7.8	1.0	1.7	2	2	48	73	821156	811504	<0.2	<0.2	0.7	0.8					
						1.0	0.1	20	17.3	8.3	8.3	30.9	30.9	97.9	97.9	7.8	1.1		3		49		<0.2				0.6								
					Middle	4.3	0.0	29	17.4	17.4	8.3	8.3	30.9	30.9	98.2	98.2	7.8	2.0	2	83	<0.2	0.9													
						4.3	0.0	21	17.4	8.3	8.3	30.9	30.9	98.2	98.2	7.8	1.9	3	83	<0.2	0.9														
					Bottom	7.6	0.0	25	17.6	17.6	8.3	8.3	30.7	30.7	99.2	99.2	7.9	7.9	2.0	87	<0.2	0.9													
						7.6	0.0	22	17.6	8.3	8.3	30.7	30.7	99.2	99.2	7.9	7.9	2.0	88	<0.2	0.8														
SR1A	Misty	Calm	11:34	5.0	Surface	1.0	0.0	359	17.7	17.7	8.2	8.2	30.4	30.3	98.7	98.8	7.8	7.8	2.7	2.9	<2	<2	-	-	819982	812664	-	-	-	-					
						1.0	-	1	17.7	8.2	8.2	30.3	30.3	98.8	98.8	7.8	2.7		<2		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.0	0.0	347	18.1	18.1	8.3	8.3	30.1	30.1	99.7	99.9	7.9	7.9	3.1	-	<2	-	-	-			-		-		-	-	-	-	
						4.0	0.0	344	18.1	8.3	8.3	30.0	30.0	100.0	100.0	7.9	7.9	3.2	<2	-	-	-	-	-			-		-		-	-	-		
SR2	Misty	Calm	11:45	5.2	Surface	1.0	0.1	45	17.9	17.9	8.3	8.3	30.8	30.8	99.1	99.1	7.8	7.8	1.4	2.0	3	3	69	78	821444	814143	<0.2	<0.2	0.9	0.8					
						1.0	0.1	41	17.9	8.3	8.3	30.8	30.8	99.1	99.1	7.8	1.5		3		69		<0.2				0.8								
					Middle	-	0.1	63	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	0.1	58	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
					Bottom	4.2	0.1	51	18.2	18.2	8.3	8.3	30.6	30.5	100.4	100.6	7.9	7.9	2.5	86	<0.2	0.8													
						4.2	0.0	50	18.2	8.3	8.3	30.5	30.5	100.7	100.7	7.9	7.9	2.5	86	<0.2	0.8														
SR3	Fine	Moderate	11:21	9.0	Surface	1.0	0.2	18	18.1	18.1	8.2	8.2	30.4	30.4	99.0	99.0	7.8	7.8	1.0	2.9	3	2	-	-	822170	807564	-	-	-	-					
						1.0	0.2	25	18.1	8.2	8.2	30.5	30.5	98.9	98.9	7.8	1.0		2		-		-				-								
					Middle	4.5	0.2	20	18.1	18.1	8.2	8.2	30.5	30.6	98.2	98.2	7.7	7.7	1.4	3	-	-	-	-			-		-		-	-	-		
						4.5	0.2	21	18.1	8.2	8.2	30.6	30.6	98.1	98.1	7.7	7.7	1.6	2	-	-	-	-	-			-		-		-	-			
					Bottom	8.0	0.1	19	18.1	18.1	8.2	8.2	31.4	31.4	98.3	98.3	7.7	7.7	6.0	-	-	-	-	-			-		-		-	-	-	-	
						8.0	0.2	25	18.1	8.2	8.2	31.4	31.4	98.3	98.3	7.7	7.7	6.3	2	-	-	-	-	-			-		-		-	-	-		
SR4A	Cloudy	Calm	12:38	9.2	Surface	1.0	0.0	358	18.3	18.3	8.3	8.3	31.6	31.6	101.0	101.0	7.9	7.9	2.2	2.4	3	4	-	-	817186	807793	-	-	-	-					
						1.0	0.1	1	18.3	8.3	8.3	31.6	31.6	101.0	101.0	7.9	2.2		4		-		-				-								
					Middle	4.6	0.1	4	18.2	18.2	8.3	8.3	31.6	31.6	100.3	100.3	7.8	7.8	2.1	4	-	-	-	-			-		-		-	-	-		
						4.6	0.1	357	18.2	8.3	8.3	31.6	31.6	100.2	100.2	7.8	7.8	2.1	5	-	-	-	-	-			-		-		-	-			
					Bottom	8.2	0.0	23	18.2	18.2	8.3	8.3	31.7	31.7	99.9	99.9	7.8	7.8	2.8	-	-	-	-	-			-		-		-	-	-		
						8.2	0.0	27	18.2	8.3	8.3	31.7	31.7	99.9	99.9	7.8	7.8	2.8	5	-	-	-	-	-			-		-		-	-	-		
SR8	Misty	Calm	11:17	4.8	Surface	1.0	-	-	17.4	17.4	8.3	8.3	30.8	30.8	98.9	98.9	7.9	7.9	2.1	2.9	5	5	-	-	820377	811632	-	-	-	-					
						1.0	-	-	17.4	8.3	8.3	30.8	30.8	98.9	98.9	7.9	2.2		6		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	3.8	-	-	17.7	17.7	8.2	8.3	30.4	30.4	100.4	103.8	8.0	8.1	3.6	-	-	-	-	-			-		-		-	-	-	-	-
						3.8	-	-	17.7	8.3	8.3	30.4	30.4	103.8	103.8	8.2	8.2	3.6	3	-	-	-	-	-			-		-		-	-	-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 15 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)				
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	
C1	Cloudy	Moderate	07:45	7.8	Surface	1.0	0.4	38	18.2	8.3	8.3	32.1	32.1	99.7	99.7	7.8	7.8	4.0	6.4	11	10	46	49	815608	804232	<0.2	0.5	0.6					
						1.0	0.3	33	18.2	8.3	8.3	32.1	32.1	99.7	99.7	7.8		4.5		12		47				<0.2			0.6				
					Middle	3.9	0.4	41	18.2	8.3	8.3	32.1	32.1	99.6	99.6	7.8	7.8	5.7	6.4	10	10	49	49			<0.2	0.6						
						3.9	0.3	35	18.2	8.3	8.3	32.1	32.1	99.6	99.6	7.8		5.7		9		50				<0.2	0.6						
					Bottom	6.8	0.4	22	18.2	8.3	8.3	32.2	32.2	99.5	99.5	7.7	7.7	9.2	6.4	10	10	51	49			<0.2	0.5						
						6.8	0.4	20	18.2	8.3	8.3	32.2	32.2	99.5	99.5	7.7		9.1		9		51				<0.2	0.6						
					C2	Cloudy	Moderate	09:08	11.7	Surface	1.0	0.3	1	18.1	8.2	8.2	30.4	30.3	97.3	97.4	7.7	7.7	0.9	2.1	<2	2	47	49	825685	806936	<0.2	0.8	0.8
											1.0	0.3	356	18.1	8.2	8.2	30.3	30.7	97.5	97.9	7.7		0.8		<2		46				<0.2	0.9	
Middle	5.9	0.3	340	18.0						8.2	8.2	30.7	30.7	97.9	97.9	7.7	1.5	1.2	2	6	49	49			<0.2	0.8							
	5.9	0.2	336	18.0						8.2	8.2	30.7	30.7	97.9	97.9	7.7	1.5		2		49				<0.2	0.8							
Bottom	10.7	0.3	329	18.1						8.3	8.3	31.6	31.6	98.2	98.2	7.7	7.7	4.0	1.2	2	6	50	72			<0.2	0.8						
	10.7	0.2	327	18.1						8.3	8.3	31.6	30.6	98.2	97.7	7.7		4.0		3		51				<0.2	0.8						
C3	Misty	Calm	07:02	12.0						Surface	1.0	0.4	266	17.3	8.2	8.2	30.6	30.6	97.6	97.6	7.8	7.8	1.0	1.2	5	6	44	72			<0.2	0.7	
											1.0	0.5	268	17.3	8.2	8.2	30.6	30.6	97.6	97.6	7.8		1.0		6		44				<0.2	0.7	
					Middle	6.0	0.4	266	17.3	8.2	8.2	30.6	30.6	97.6	97.6	7.8	7.8	1.2	1.2	5	6	86	48			<0.2	0.8						
						6.0	0.5	262	17.3	8.2	8.2	30.6	30.6	97.6	97.6	7.8		1.1		6		86				<0.2	0.7						
					Bottom	11.0	0.4	285	17.3	8.2	8.2	30.6	30.6	97.6	97.7	7.8	7.8	1.5	1.2	6	6	87	48			<0.2	0.7						
						11.0	0.4	291	17.3	8.2	8.2	30.6	30.6	97.8	97.7	7.8		1.5		6		87				<0.2	0.6						
IM1	Fine	Moderate	08:03	6.5	Surface	1.0	0.2	15	18.0	8.3	8.3	31.2	31.2	99.1	99.1	7.8	7.8	2.8	2.9	6	6	45	48	818354	806454	<0.2	0.6	0.6					
						1.0	0.2	20	18.0	8.3	8.3	31.2	31.2	99.1	99.0	7.8		2.8		5		45				<0.2	0.6						
					Middle	3.3	0.2	28	18.0	8.3	8.3	31.2	31.2	99.0	99.0	7.8	7.8	3.0	3.2	6	5	48	49			<0.2	0.7						
						3.3	0.2	25	18.0	8.3	8.3	31.2	31.2	99.0	99.0	7.8		2.9		5		49				<0.2	0.7						
					Bottom	5.5	0.2	37	18.0	8.3	8.3	31.2	31.2	99.1	99.1	7.8	7.8	3.1	3.2	6	5	50	48			<0.2	0.6						
						5.5	0.2	36	18.0	8.3	8.3	31.2	31.2	99.1	99.1	7.8		3.1		6		49				<0.2	0.6						
IM2	Fine	Moderate	08:09	7.4	Surface	1.0	0.2	14	17.9	8.3	8.3	31.2	31.2	98.7	98.7	7.8	7.8	2.6	3.2	4	5	46	48	819170	806250	<0.2	0.6	0.6					
						1.0	0.2	15	17.9	8.3	8.3	31.2	31.2	98.7	98.7	7.8		2.6		4		45				<0.2	0.7						
					Middle	3.7	0.3	30	18.1	8.3	8.3	31.7	31.7	98.6	98.6	7.7	7.7	3.0	3.2	5	6	48	49			<0.2	0.6						
						3.7	0.3	30	18.1	8.3	8.3	31.7	31.7	98.5	98.6	7.7		3.2		6		48				<0.2	0.6						
					Bottom	6.4	0.3	27	18.1	8.3	8.3	31.8	31.8	98.6	98.6	7.7	7.7	3.9	1.0	6	4	50	48			<0.2	0.6						
						6.4	0.3	26	18.1	8.3	8.3	31.8	30.2	98.6	97.1	7.7		3.9		5		49				<0.2	0.6						
IM7	Cloudy	Moderate	08:30	8.1	Surface	1.0	0.2	348	18.0	8.2	8.2	30.1	30.1	97.8	97.8	7.7	7.7	0.8	1.0	2	4	45	48	821348	806821	<0.2	0.8	0.8					
						1.0	0.2	352	18.0	8.2	8.2	30.1	30.1	97.8	97.3	7.7		0.8		3		45				<0.2	0.8						
					Middle	4.1	0.2	0	18.0	8.2	8.2	30.1	30.1	97.3	97.3	7.7	7.7	1.0	1.0	4	4	49	49			<0.2	0.9						
						4.1	0.2	7	18.0	8.2	8.2	30.1	30.1	97.3	97.3	7.7		1.1		4		49				<0.2	0.9						
					Bottom	7.1	0.2	336	18.0	8.2	8.2	30.2	30.2	97.1	97.1	7.7	7.7	1.3	1.3	5	4	50	48			<0.2	0.8						
						7.1	0.2	336	18.0	8.2	8.2	30.2	30.2	97.1	97.1	7.7		1.3		4		50				<0.2	0.8						

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 15 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)									
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA				
IM10	Misty	Calm	07:57	7.4	Surface	1.0	0.4	305	17.2	17.2	8.2	8.2	30.7	30.7	97.6	97.6	7.8	7.8	1.9	2.3	3	3	49	73	822223	809824	<0.2	<0.2	0.7	0.9								
						1.0	0.4	298	17.2	8.2	8.2	30.7	30.7	97.6	97.6	7.8	1.9		2		48		<0.2				0.7											
					Middle	3.7	0.3	299	17.2	17.2	8.2	8.2	30.7	30.7	97.6	97.7	7.8		2.0		3		83				<0.2		0.7									
						3.7	0.3	299	17.2	8.2	8.2	30.7	30.7	97.7	97.7	7.8	2.0		2		83		<0.2				0.7											
					Bottom	6.4	0.4	277	17.2	17.2	8.2	8.2	30.7	30.7	97.7	97.7	7.8	2.9	4	86	<0.2	1.3																
						6.4	0.4	269	17.2	17.2	8.2	8.2	30.7	30.7	97.8	97.8	7.8	2.9	3	86	<0.2	1.3																
					IM11	Misty	Calm	07:51	7.6	Surface	1.0	0.4	269	17.2	17.2	8.2	8.2	30.7	30.7	97.7	97.7	7.8	7.8	2.1			4.0	4	4		48	75	821507	810527	<0.2	<0.2	1.2	1.1
											1.0	0.4	273	17.2	8.2	8.2	30.7	30.7	97.7	97.7	7.8	2.2		4				48			<0.2				1.2			
Middle	3.8	0.4	270	17.2						17.2	8.2	8.2	30.7	30.7	97.7	97.7	7.8	4.0	3	86	<0.2	1.3																
	3.8	0.5	265	17.2						8.2	8.2	30.7	30.7	97.7	97.7	7.8	4.1	4	86	<0.2	1.4																	
Bottom	6.6	0.4	275	17.2						17.2	8.2	8.2	30.7	30.6	97.8	97.8	7.8	7.8	5.9	3	90	<0.2	0.8															
	6.6	0.4	276	17.2						8.2	8.2	30.6	30.6	97.8	97.8	7.8	7.8	5.7	4	90	<0.2	0.9																
IM12	Misty	Calm	07:43	8.4						Surface	1.0	0.4	289	17.3	17.3	8.2	8.2	31.0	31.0	95.7	95.7	7.6	7.6	1.5	2.6	4	3	45	73	821158	811525	<0.2			<0.2	1.4	1.3	
											1.0	0.4	294	17.3	8.2	8.2	31.0	31.0	95.6	95.7	7.6	1.4		4		45		<0.2				1.3						
					Middle	4.2	0.4	296	17.3	17.3	8.2	8.2	31.0	31.0	95.8	95.8	7.6	2.4	3	86	<0.2	1.4																
						4.2	0.4	297	17.3	8.2	8.2	31.0	31.0	95.8	95.8	7.6	2.5	4	86	<0.2	1.3																	
					Bottom	7.4	0.4	282	17.2	17.2	8.2	8.2	31.0	31.0	96.2	96.2	7.7	7.7	3.9	2	87	<0.2	1.3															
						7.4	0.5	275	17.2	8.2	8.2	31.0	31.0	96.2	96.2	7.7	7.7	3.8	3	87	<0.2	1.3																
					SR1A	Misty	Calm	07:18	5.0	Surface	1.0	0.0	187	17.2	17.2	8.2	8.2	30.6	30.6	94.9	95.0	7.6	7.6	1.5	2.0	5	5	-	-			819970	812657	-	-	-		-
											1.0	0.0	194	17.2	8.2	8.2	30.6	30.6	95.0	95.0	7.6	1.6		4		-		-						-		-		
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-																
	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-																
Bottom	4.0	0.0	178	17.2						17.2	8.2	8.2	30.6	30.6	95.5	95.5	7.6	7.6	2.5	4	-	-	-	-	-	-	-	-	-									
	4.0	0.0	175	17.2						8.2	8.2	30.6	30.6	95.5	95.5	7.6	7.6	2.5	5	-	-	-	-	-	-	-	-											
SR2	Misty	Calm	07:05	5.0						Surface	1.0	0.1	257	17.3	17.3	8.1	8.1	30.7	30.7	89.3	89.3	7.1	7.1	2.3	3.0	<2	<2	43	65	821467	814187			<0.2	<0.2	1.3	1.3	
											1.0	0.1	254	17.3	8.1	8.1	30.7	30.7	89.2	89.3	7.1	2.4		43		<0.2		1.3										
					Middle	-	0.0	251	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-	-	-				
						-	0.0	256	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-				-	-					
					Bottom	4.0	0.0	256	17.3	17.3	8.1	8.1	30.6	30.6	66.4	65.5	5.3	5.3	3.7	<2	87	<0.2	1.3															
						4.0	0.0	254	17.3	8.1	8.1	30.6	30.6	64.5	65.5	5.2	5.2	3.8	<2	87	<0.2	1.3																
					SR3	Cloudy	Moderate	08:43	8.6	Surface	1.0	0.3	331	18.0	18.0	8.2	8.2	30.2	30.2	97.2	97.2	7.7	7.7	0.9	1.0	2	4	-	-			822165	807548	-	-	-		-
											1.0	0.3	338	18.0	8.2	8.2	30.2	30.2	97.1	97.1	7.7	0.9		3		-		-						-				
Middle	4.3	0.3	356	18.1						18.1	8.2	8.2	30.3	30.3	96.7	96.7	7.6	7.6	0.8	4	-	-		-		-		-		-								
	4.3	0.3	353	18.1						8.2	8.2	30.3	30.3	96.7	96.7	7.6	7.6	0.8	5	-	-	-		-		-		-										
Bottom	7.6	0.3	334	18.1						18.1	8.2	8.2	30.3	30.3	96.5	96.5	7.6	7.6	1.3	4	-	-	-	-	-	-	-	-										
	7.6	0.3	329	18.1						8.2	8.2	30.3	30.3	96.5	96.5	7.6	7.6	1.3	5	-	-	-	-	-	-	-	-											
SR4A	Cloudy	Calm	07:23	9.0						Surface	1.0	0.0	220	18.1	18.1	8.2	8.2	30.6	30.6	98.0	98.0	7.7	7.7	2.0	2.0	6	6	-	-	817185	807830			-	-	-	-	
											1.0	0.0	222	18.1	8.2	8.2	30.6	30.6	98.0	98.0	7.7	2.0		7		-		-						-		-		
					Middle	4.5	0.0	194	18.1	18.1	8.2	8.2	30.6	30.6	97.8	97.8	7.7	2.0	5	-	-	-		-		-		-				-						
						4.5	0.0	198	18.1	8.2	8.2	30.6	30.6	97.8	97.8	7.7	1.9	6	-	-	-	-		-		-		-										
					Bottom	8.0	0.0	208	18.1	18.1	8.2	8.2	30.6	30.6	97.6	97.6	7.7	7.7	2.2	4	-	-	-	-	-	-	-	-										
						8.0	0.0	206	18.1	8.2	8.2	30.6	30.6	97.6	97.6	7.7	7.7	2.1	5	-	-	-	-	-	-	-	-											
					SR8	Misty	Calm	07:35	5.0	Surface	1.0	-	-	17.2	17.2	8.4	8.4	30.2	30.2	95.3	95.3	7.7	7.7	1.8	2.2	2	3	-	-			820379	811606	-	-	-		-
											1.0	-	-	17.2	8.4	8.4	30.1	30.1	95.3	95.3	7.6	1.9		3		-		-						-				
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-		-	-			-				
	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-		-		-		-		-	-							
Bottom	4.0	-	-	17.2						17.2	8.3	8.3	29.3	29.3	95.1	95.1	7.7	7.7	2.5	3	-	-	-	-	-	-	-	-	-									
	4.0	-	-	17.2						8.3	8.3	29.2	29.2	95.1	95.1	7.7	7.7	2.5	3	-	-	-	-	-	-	-	-	-										

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 17 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)		
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value
C1	Rainy	Moderate	13:23	8.6	Surface	1.0	0.2	207	17.0	17.0	8.3	8.3	32.3	32.3	99.1	99.1	7.9	7.9	3.4	4.7	3	3	51	75	815618	804227	0.2	0.2	0.5	0.6	
						1.0	0.2	203	17.0	17.0	8.3	8.3	32.3	32.3	99.1	99.1	7.9		3.5		3		51				0.2		0.6		
					Middle	4.3	0.1	206	17.0	17.0	8.3	8.3	32.5	32.5	98.7	98.7	7.8	7.8	4.6	3	86	0.2	0.5								
						4.3	0.2	210	17.0	17.0	8.3	8.3	32.5	32.5	98.7	98.7	7.8	7.8	4.5	3	86	0.2	0.6								
					Bottom	7.6	0.2	208	17.0	17.0	8.4	8.4	32.5	32.5	98.7	98.7	7.8	7.8	6.0	3	88	0.2	0.7								
						7.6	0.2	202	17.0	17.0	8.4	8.4	32.5	32.5	98.6	98.7	7.8	7.8	5.9	3	87	0.2	0.6								
C2	Rainy	Moderate	12:01	12.0	Surface	1.0	0.0	13	17.4	17.4	8.3	8.3	30.4	30.4	97.9	97.9	7.8	7.8	1.3	1.7	3	3	44	73	825699	806924	0.3	0.2	0.5	0.6	
						1.0	0.0	11	17.4	17.4	8.3	8.3	30.4	30.4	97.9	97.9	7.8		1.3		3		44				0.3		0.6		
					Middle	6.0	0.1	0	17.4	17.4	8.3	8.3	30.6	30.6	97.6	97.6	7.8	7.8	1.5	3	86	0.2	0.7								
						6.0	0.1	359	17.4	17.4	8.3	8.3	30.6	30.6	97.6	97.6	7.8	7.8	1.5	2	86	0.2	0.7								
					Bottom	11.0	0.1	8	17.4	17.4	8.3	8.3	30.4	30.4	97.5	97.5	7.8	7.8	2.2	2	90	0.2	0.6								
						11.0	0.1	0	17.4	17.4	8.3	8.3	30.4	30.4	97.5	97.5	7.8	7.8	2.3	2	90	0.2	0.6								
C3	Rainy	Rough	13:38	11.0	Surface	1.0	0.3	101	18.1	18.1	8.2	8.2	31.9	31.9	96.3	96.3	7.5	7.5	7.1	2.9	3	2	47	49	822116	817807	0.2	0.2	0.6	0.6	
						1.0	0.3	107	18.1	18.1	8.2	8.2	31.9	31.9	96.2	96.3	7.5		7.1		3		46				0.3		0.6		
					Middle	5.5	0.3	88	18.1	18.1	8.2	8.2	32.2	32.2	95.5	95.5	7.5	7.5	0.7	2	48	0.2	0.6								
						5.5	0.2	83	18.1	18.1	8.2	8.2	32.2	32.2	95.5	95.5	7.5	7.5	0.7	2	49	0.2	0.6								
					Bottom	10.0	0.3	98	18.0	18.0	8.2	8.2	32.2	32.2	96.7	96.9	7.6	7.6	0.8	2	51	0.2	0.6								
						10.0	0.3	90	18.0	18.0	8.2	8.2	32.2	32.2	97.0	96.9	7.6	7.6	0.8	2	52	0.2	0.5								
IM1	Rainy	Moderate	13:07	7.8	Surface	1.0	0.1	167	17.3	17.3	8.3	8.3	31.3	31.3	99.0	99.0	7.9	7.9	1.0	1.6	5	3	48	74	818366	806451	0.2	0.2	1.0	1.0	
						1.0	0.0	165	17.3	17.3	8.3	8.3	31.3	31.3	99.0	99.0	7.9		1.1		4		48				0.2		0.9		
					Middle	3.9	0.1	135	17.3	17.3	8.3	8.3	31.3	31.3	98.9	98.9	7.9	7.9	1.4	3	86	<0.2	1.0								
						3.9	0.1	135	17.3	17.3	8.3	8.3	31.3	31.3	98.9	98.9	7.9	7.9	1.5	3	86	<0.2	0.9								
					Bottom	6.8	0.0	153	17.3	17.3	8.3	8.3	31.3	31.3	98.8	98.9	7.9	7.9	2.3	2	88	0.2	1.0								
						6.8	0.0	147	17.3	17.3	8.3	8.3	31.3	31.3	98.9	98.9	7.9	7.9	2.5	2	88	0.3	1.0								
IM2	Rainy	Moderate	13:01	7.6	Surface	1.0	0.0	111	17.3	17.3	8.4	8.4	31.5	31.5	98.3	98.3	7.8	7.8	2.1	3.8	8	8	49	71	819185	806255	0.2	0.2	0.9	0.9	
						1.0	0.0	112	17.3	17.3	8.4	8.4	31.5	31.5	98.3	98.3	7.8		2.1		8		49				0.2		0.9		
					Middle	3.8	0.0	121	17.2	17.2	8.4	8.4	31.6	31.6	98.1	98.1	7.8	7.8	4.0	8	78	0.2	0.9								
						3.8	0.0	122	17.2	17.2	8.4	8.4	31.6	31.6	98.1	98.1	7.8	7.8	4.0	8	79	0.2	1.0								
					Bottom	6.6	0.0	81	17.2	17.2	8.4	8.5	31.7	31.7	97.8	97.8	7.8	7.8	5.3	9	84	0.2	0.9								
						6.6	0.0	87	17.2	17.2	8.5	8.5	31.7	31.7	97.8	97.8	7.8	7.8	5.3	9	85	0.2	0.9								
IM7	Rainy	Moderate	12:43	8.6	Surface	1.0	0.2	51	17.3	17.3	8.3	8.3	31.1	31.1	97.4	97.4	7.8	7.8	1.1	1.4	11	10	52	77	821330	806841	0.2	0.2	0.8	0.9	
						1.0	0.2	54	17.3	17.3	8.3	8.3	31.1	31.1	97.4	97.4	7.8		1.0		11		52				0.2		0.9		
					Middle	4.3	0.2	82	17.3	17.3	8.3	8.3	31.2	31.2	97.5	97.5	7.8	7.8	1.1	9	88	0.2	0.9								
						4.3	0.2	84	17.3	17.3	8.3	8.3	31.2	31.2	97.5	97.5	7.8	7.8	1.2	9	88	0.2	0.9								
					Bottom	7.6	0.2	62	17.3	17.3	8.3	8.3	31.3	31.3	97.6	97.7	7.8	7.8	1.9	9	90	0.2	0.9								
						7.6	0.3	59	17.3	17.3	8.3	8.3	31.3	31.3	97.7	97.7	7.8	7.8	1.8	9	90	0.2	0.9								

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Water Quality Monitoring

Water Quality Monitoring Results on 17 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)										
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	Value	DA			
IM10	Rainy	Rough	11:58	7.8	Surface	1.0	0.1	33	18.2	18.2	8.2	8.2	30.7	30.7	97.9	97.9	7.7	7.7	5.6	2.6	5	6	47	49	822257	809843	0.2	0.2	1.2	1.0									
						1.0	0.0	28	18.2	8.2	8.2	30.7	97.9	7.7	5.5	5	47	0.2	1.2																				
					Middle	3.9	0.1	24	18.2	8.2	8.2	31.2	31.2	97.4	97.4	7.6	7.6	1.0	5	49	<0.2	0.8																	
						3.9	0.1	25	18.2	8.2	8.2	31.3	31.2	97.4	97.4	7.6	7.6	1.1	6	47	<0.2	0.7																	
					Bottom	6.8	0.0	40	18.2	8.2	8.2	31.4	31.4	97.6	97.6	7.6	7.6	1.2	6	51	<0.2	0.9																	
						6.8	0.0	45	18.2	8.2	8.2	31.4	31.4	97.7	97.7	7.6	7.6	1.1	7	51	<0.2	0.9																	
					IM11	Rainy	Rough	12:21	7.7	Surface	1.0	0.1	66	18.2	18.2	8.2	8.2	31.5	31.5	99.1	99.1	7.7	7.7	1.0			1.2		5		4	47	49	821517	810548	<0.2	<0.2	0.6	0.6
											1.0	0.0	68	18.2	8.2	8.2	31.5	31.5	99.1	99.1	7.7	7.7	1.0	4					48			<0.2				0.6			
Middle	3.9	0.1	66	18.1						18.1	8.2	8.2	31.5	31.5	99.2	99.3	7.8	7.8	1.2	4	49	<0.2	0.6																
	3.9	0.1	69	18.1						18.1	8.2	8.2	31.5	31.5	99.3	99.3	7.8	7.8	1.2	3	48	<0.2	0.7																
Bottom	6.7	0.1	44	18.1						18.1	8.2	8.2	31.5	31.5	99.6	99.7	7.8	7.8	1.3	3	51	<0.2	0.6																
	6.7	0.1	37	18.1						18.1	8.2	8.2	31.5	31.5	99.7	99.7	7.8	7.8	1.4	3	51	<0.2	0.7																
IM12	Rainy	Rough	12:28	8.4						Surface	1.0	0.2	79	18.2	18.2	8.2	8.2	31.5	31.5	97.8	97.8	7.6	7.7	1.1	1.1	5	4	47	49	821157	811537	<0.2	<0.2			0.6		0.6	
											1.0	0.2	75	18.2	8.2	8.2	31.5	31.5	97.8	97.8	7.6	7.7	1.1	5		47		<0.2				0.6							
					Middle	4.2	0.2	91	18.2	18.2	8.2	8.2	31.5	31.5	97.8	97.9	7.7	7.7	1.1	4	49	<0.2	0.6																
						4.2	0.2	87	18.2	18.2	8.2	8.2	31.5	31.5	97.9	97.9	7.7	7.7	1.1	4	48	<0.2	0.6																
					Bottom	7.4	0.1	66	18.2	18.2	8.2	8.2	31.5	31.5	98.1	98.1	7.7	7.7	1.2	3	51	<0.2	0.6																
						7.4	0.1	63	18.2	18.2	8.2	8.2	31.5	31.5	98.1	98.1	7.7	7.7	1.2	3	51	<0.2	0.5																
					SR1A	Rainy	Rough	12:59	4.3	Surface	1.0	0.0	12	18.2	18.2	8.2	8.2	31.3	31.3	98.0	98.0	7.7	7.7	0.9	0.8	2	2	-	-			819974		812661	-	-	-		-
											1.0	0.0	5	18.2	8.2	8.2	31.4	31.4	98.0	98.0	7.7	7.7	0.9	2		-		-							-				
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-									
	3.3	0.1	17	18.2						18.2	8.2	8.2	31.4	31.4	98.7	98.7	7.7	7.7	0.8	3	-	-	-	-	-	-	-	-	-										
Bottom	3.3	0.1	23	18.1						18.2	8.2	8.2	31.4	31.4	98.7	98.7	7.7	7.7	0.8	2	-	-	-	-	-	-	-	-	-	-									
	3.3	0.1	23	18.1						18.2	8.2	8.2	31.4	31.4	98.7	98.7	7.7	7.7	0.8	2	-	-	-	-	-	-	-	-	-										
SR2	Rainy	Rough	13:16	4.5						Surface	1.0	0.1	55	18.1	18.1	8.2	8.2	31.5	31.5	99.3	99.3	7.8	7.8	1.0	1.5	2	3	48	49	821458	814173		<0.2		<0.2		0.7	0.6	
											1.0	0.2	52	18.1	8.2	8.2	31.5	31.5	99.3	99.3	7.8	7.8	1.0	2		47		<0.2					0.6						
					Middle	-	0.2	69	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-							
						-	0.1	62	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-										
					Bottom	3.5	0.2	53	18.1	18.1	8.2	8.2	31.5	31.5	99.9	100.0	7.8	7.8	2.0	3	51	<0.2	0.6																
						3.5	0.2	51	18.1	18.1	8.2	8.2	31.5	31.5	100.0	100.0	7.8	7.8	2.2	3	50	<0.2	0.6																
					SR3	Rainy	Moderate	12:37	8.8	Surface	1.0	0.1	38	17.4	17.4	8.3	8.3	30.6	30.6	98.2	98.2	7.8	7.8	1.1	1.6	4	3	-	-			822132	807576	-		-	-		-
											1.0	0.2	33	17.4	8.3	8.3	30.6	98.1	98.1	7.8	7.8	1.1	4	-		-		-											
Middle	4.4	0.1	31	17.4						17.4	8.3	8.3	30.7	30.7	98.0	98.0	7.8	7.8	1.5	4	-	-	-	-	-	-	-	-											
	4.4	0.1	38	17.4						17.4	8.3	8.3	30.7	30.7	98.0	98.0	7.8	7.8	1.6	3	-	-	-	-	-	-	-	-											
Bottom	7.8	0.1	44	17.4						17.4	8.3	8.3	30.7	30.7	98.1	98.1	7.8	7.8	2.1	2	-	-	-	-	-	-	-	-	-										
	7.8	0.1	41	17.4						17.4	8.3	8.3	30.7	30.7	98.1	98.1	7.8	7.8	2.1	2	-	-	-	-	-	-	-	-											
SR4A	Rainy	Moderate	13:46	9.0						Surface	1.0	0.0	72	17.1	17.1	8.3	8.3	32.2	32.2	99.4	99.4	7.9	7.9	4.1	5.1	5	4	-	-	817211	807828			-	-		-	-	
											1.0	0.0	71	17.1	8.3	8.3	32.2	99.4	99.4	7.9	7.9	4.2	5	-		-		-											
					Middle	4.5	0.0	70	17.0	17.0	8.3	8.3	32.4	32.4	99.3	99.4	7.9	7.9	5.1	4	-	-	-	-	-	-	-	-	-										
						4.5	-	69	17.0	17.0	8.3	8.3	32.4	32.4	99.4	99.4	7.9	7.9	5.1	4	-	-	-	-	-	-	-	-											
					Bottom	8.0	0.0	64	17.0	17.0	8.3	8.3	32.2	32.2	99.7	99.7	7.9	7.9	6.0	3	-	-	-	-	-	-	-	-	-										
						8.0	0.0	64	17.0	17.0	8.3	8.3	32.2	32.2	99.7	99.7	7.9	7.9	6.1	3	-	-	-	-	-	-	-	-											
					SR8	Rainy	Rough	12:35	4.1	Surface	1.0	-	-	18.2	18.2	8.2	8.2	31.4	31.4	99.4	99.4	7.8	7.8	2.0	4.7	6	5	-	-			820402	811615	-		-	-		-
											1.0	-	-	18.2	8.2	8.2	31.4	31.4	99.4	99.4	7.8	7.8	2.0	6		-		-						-					
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-									
	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-										
Bottom	3.1	-	-	18.2						18.2	8.2	8.2	31.4	31.4	99.7	99.8	7.8	7.8	7.4	5	-	-	-	-	-	-	-	-	-	-									
	3.1	-	-	18.2						18.2	8.2	8.2	31.5	31.4	99.8	99.8	7.8	7.8	7.4	4	-	-	-	-	-	-	-	-	-										

DA: Depth-Averaged

Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

Value exceeding Action Level is underlined; Value exceeding Limit Level is bolded and underlined

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 17 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Rainy	Moderate	08:59	9.0	Surface	1.0	0.4	23	17.1	17.1	8.2	8.2	31.9	31.9	98.4	98.4	7.8	7.8	7.1	8.1	4	3	46	73	815626	804256	<0.2	<0.2	0.7	0.7
						1.0	0.4	24	17.1		8.2	8.2	31.9	31.9	98.4	98.4	7.8		7.2		5		46				<0.2		0.6	
					Middle	4.5	0.4	33	17.1	17.1	8.2	8.2	31.9	31.9	98.4	98.4	7.8	7.8	8.2		3		86				<0.2		0.7	
						4.5	0.4	26	17.1		8.2	8.2	31.9	31.9	98.4	98.4	7.8		8.1		3		86				<0.2		0.6	
					Bottom	8.0	0.4	52	17.1	17.2	8.2	8.2	31.9	31.9	98.4	98.4	7.8	7.8	9.1		2		87				<0.2		0.6	
						8.0	0.4	47	17.2		8.2	8.2	31.9	31.9	98.4	98.4	7.8		9.0		3		87				<0.2		0.7	
					Surface	1.0	0.3	340	17.5	17.5	8.2	8.2	29.9	29.9	96.8	96.8	7.7	7.7	1.1	1.7	7	6	44	74	825660	806929	<0.2	<0.2	0.9	0.9
						1.0	0.3	335	17.5		8.2	8.2	29.9	29.9	96.8	96.8	7.7		1.1		7		45				<0.2		1.0	
C2	Rainy	Moderate	10:06	12.2	Middle	6.1	0.3	357	17.4	17.4	8.3	8.3	30.0	30.1	96.4	96.4	7.7	7.7	1.8		6		86				<0.2		0.9	
						6.1	0.3	4	17.4		8.3	8.3	30.1	30.1	96.3	96.3	7.7		1.8		6		86				<0.2		1.0	
					Bottom	11.2	0.3	9	17.4	17.4	8.3	8.3	30.0	30.0	96.3	96.3	7.7	7.7	2.3		5		90				<0.2		0.9	
						11.2	0.3	4	17.4		8.3	8.3	30.0	30.0	96.3	96.3	7.7		2.2		5		90				<0.2		0.9	
C3	Rainy	Moderate	08:13	10.8	Surface	1.0	0.4	278	18.2	18.2	8.1	8.1	31.6	31.6	96.4	96.4	7.5	7.5	2.2	7.3	4	5	45	48	822091	817801	<0.2	<0.2	0.8	0.7
						1.0	0.4	282	18.2		8.1	8.1	31.6	31.6	96.4	96.4	7.5		2.3		4		46				<0.2		0.8	
					Middle	5.4	0.5	260	18.2	18.2	8.1	8.1	31.7	31.7	96.3	96.3	7.5	7.5	7.9		4		48				<0.2		0.6	
						5.4	0.4	257	18.2		8.1	8.1	31.7	31.7	96.3	96.3	7.5		8.0		5		47				<0.2		0.7	
					Bottom	9.8	0.5	277	18.2	18.2	8.1	8.1	31.7	31.7	96.3	96.3	7.5	7.5	11.1		6		51				<0.2		0.6	
						9.8	0.4	280	18.2		8.1	8.1	31.7	31.7	96.3	96.3	7.5		11.9		7		51				<0.2		0.6	
IM1	Rainy	Moderate	09:17	6.8	Surface	1.0	0.3	12	17.4	17.4	8.3	8.3	31.3	31.3	97.5	97.5	7.7	7.7	2.8	3.7	4	4	53	77	818350	806439	<0.2	<0.2	0.9	0.9
						1.0	0.3	11	17.4		8.3	8.3	31.3	31.3	97.5	97.5	7.7		2.8		5		52				<0.2		0.9	
					Middle	3.4	0.3	356	17.4	17.4	8.3	8.3	31.3	31.3	97.4	97.4	7.7	7.7	3.5		4		87				<0.2		0.8	
						3.4	0.2	351	17.4		8.3	8.3	31.3	31.3	97.3	97.3	7.7		3.5		4		87				<0.2		0.8	
					Bottom	5.8	0.2	10	17.4	17.4	8.3	8.3	31.3	31.3	97.2	97.2	7.7	7.7	4.8		4		90				<0.2		0.9	
						5.8	0.2	12	17.4		8.3	8.3	31.3	31.3	97.2	97.2	7.7		4.8		4		90				<0.2		0.9	
IM2	Rainy	Moderate	09:24	7.8	Surface	1.0	0.4	7	17.3	17.3	8.3	8.3	31.4	31.4	97.0	97.0	7.7	7.7	2.0	2.8	5	5	49	74	819163	806241	<0.2	<0.2	0.9	0.9
						1.0	0.4	1	17.3		8.3	8.3	31.4	31.4	96.9	96.9	7.7		2.1		6		49				<0.2		0.9	
					Middle	3.9	0.3	2	17.3	17.3	8.3	8.3	31.4	31.4	96.5	96.5	7.7	7.7	2.5		5		86				<0.2		0.8	
						3.9	0.4	358	17.3		8.3	8.3	31.4	31.4	96.4	96.4	7.7		2.5		5		86				<0.2		0.9	
					Bottom	6.8	0.3	16	17.2	17.2	8.3	8.3	31.5	31.5	95.5	95.5	7.6	7.6	3.8		5		87				<0.2		0.9	
						6.8	0.4	22	17.2		8.3	8.3	31.5	31.5	95.3	95.4	7.6		3.6		5		87				<0.2		1.0	
IM7	Rainy	Moderate	09:42	8.8	Surface	1.0	0.2	27	17.4	17.4	8.3	8.3	30.7	30.7	96.1	96.1	7.7	7.7	1.0	1.9	5	6	50	77	821360	806848	<0.2	<0.2	0.9	0.9
						1.0	0.3	30	17.4		8.3	8.3	30.7	30.7	96.0	96.0	7.7		1.1		5		51				<0.2		0.8	
					Middle	4.4	0.3	29	17.4	17.4	8.3	8.3	30.7	30.7	95.8	95.8	7.6	7.6	1.8		5		90				<0.2		0.8	
						4.4	0.3	36	17.4		8.3	8.3	30.7	30.7	95.8	95.8	7.6		1.8		5		90				<0.2		1.0	
					Bottom	7.8	0.3	23	17.4	17.4	8.3	8.3	30.5	30.5	95.6	95.6	7.6	7.6	2.8		6		91				<0.2		0.9	
						7.8	0.3	21	17.4		8.3	8.3	30.5	30.5	95.6	95.6	7.6		2.8		7		91				<0.2		0.9	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 17 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)						
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA			
IM10	Cloudy	Moderate	09:34	7.8	Surface	1.0	0.3	313	18.2	18.2	8.2	8.2	31.4	31.4	98.6	98.6	7.7	7.7	1.7	2.0	4	5	46	48	822221	809860	<0.2	<0.2	0.7	0.6					
						1.0	0.3	306	18.2	8.2	8.2	31.4	31.4	98.6	98.6	7.7	1.8		47		<0.2		0.7												
					Middle	3.9	0.3	310	18.2	18.2	8.2	8.2	31.4	31.4	98.6	98.7	7.7	1.9	5	48	<0.2	0.6													
						3.9	0.3	313	18.2	8.2	8.2	31.4	31.4	98.7	98.7	7.7	1.9	5	48	<0.2	0.6														
					Bottom	6.8	0.3	309	18.2	18.2	8.2	8.2	31.5	31.4	99.2	99.3	7.8	7.8	2.3	51	<0.2	0.6													
						6.8	0.4	302	18.2	8.2	8.2	31.4	31.4	99.3	99.3	7.8	7.8	2.4	50	<0.2	0.6														
IM11	Cloudy	Moderate	09:27	8.0	Surface	1.0	0.4	270	18.2	18.2	8.2	8.2	31.5	31.5	98.0	98.0	7.7	7.7	3.0	3.0	5	7	47	48	821480	810537	<0.2	<0.2	0.6	0.6					
						1.0	0.3	265	18.2	8.2	8.2	31.5	31.5	98.0	98.0	7.7	3.0		47		<0.2		0.6												
					Middle	4.0	0.4	292	18.2	18.2	8.2	8.2	31.5	31.5	98.1	98.1	7.7	2.9	7	48	<0.2	0.6													
						4.0	0.3	289	18.2	8.2	8.2	31.5	31.5	98.1	98.1	7.7	3.0	7	47	<0.2	0.6														
					Bottom	7.0	0.4	265	18.2	18.2	8.2	8.2	31.5	31.5	98.3	98.4	7.7	7.7	3.0	50	<0.2	0.7													
						7.0	0.4	265	18.2	8.2	8.2	31.5	31.5	98.4	98.4	7.7	7.7	3.1	51	<0.2	0.7														
IM12	Cloudy	Moderate	09:20	8.4	Surface	1.0	0.4	278	18.2	18.2	8.2	8.2	31.4	31.4	98.0	98.0	7.7	7.7	1.8	5.7	7	5	46	48	821166	811497	<0.2	<0.2	0.7	0.7					
						1.0	0.4	282	18.2	8.2	8.2	31.4	31.4	97.9	97.9	7.7	1.9		6		47		<0.2				0.7								
					Middle	4.2	0.4	277	18.2	18.2	8.2	8.2	31.5	31.5	97.9	97.9	7.7	6.8	5	48	<0.2	0.6													
						4.2	0.3	275	18.2	8.2	8.2	31.5	31.5	97.9	97.9	7.7	7.2	5	47	<0.2	0.6														
					Bottom	7.4	0.4	263	18.2	18.2	8.2	8.2	31.5	31.5	98.0	98.0	7.7	7.7	8.7	51	<0.2	0.7													
						7.4	0.4	262	18.2	8.2	8.2	31.5	31.5	98.0	98.0	7.7	7.7	8.2	50	<0.2	0.7														
SR1A	Rainy	Moderate	08:47	5.6	Surface	1.0	-	208	18.2	18.2	8.2	8.2	31.3	31.3	96.1	96.2	7.5	7.5	1.5	3.0	4	3	-	-	819978	812656	-	-	-	-					
						1.0	0.0	202	18.2	8.2	8.2	31.3	31.3	96.2	96.2	7.5	1.5		4		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.6	0.0	207	18.2	18.2	8.2	8.2	31.3	31.3	96.4	96.5	7.5	7.5	4.4	2	-	-	-	-			-		-		-	-	-	-	
						4.6	0.0	204	18.2	8.2	8.2	31.3	31.3	96.5	96.5	7.5	7.5	4.6	2	-	-	-	-	-			-		-		-	-	-	-	
SR2	Rainy	Moderate	08:31	3.6	Surface	1.0	0.1	235	18.2	18.2	8.2	8.2	31.5	31.5	98.5	98.6	7.7	7.7	3.4	3.7	4	6	47	49	821446	814174	<0.2	<0.2	0.6	0.7					
						1.0	0.1	234	18.2	8.2	8.2	31.5	31.5	98.6	98.6	7.7	3.6		5		48		<0.2				0.7								
					Middle	-	0.1	256	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	0.1	251	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
					Bottom	2.6	0.0	241	18.1	18.1	8.2	8.2	31.5	31.5	99.4	99.5	7.8	7.8	3.9	7	50	<0.2	0.6												
						2.6	0.0	240	18.1	8.2	8.2	31.5	31.5	99.5	99.5	7.8	7.8	3.8	7	50	<0.2	0.7													
SR3	Rainy	Moderate	09:49	9.2	Surface	1.0	0.3	346	17.5	17.5	8.2	8.2	30.2	30.2	96.1	96.1	7.7	7.7	1.1	1.3	6	5	-	-	822150	807554	-	-	-	-					
						1.0	0.4	344	17.5	8.2	8.2	30.3	30.3	96.1	96.1	7.7	1.0		6		-		-				-								
					Middle	4.6	0.3	339	17.5	17.5	8.2	8.2	30.3	30.3	95.8	95.8	7.6	7.6	1.2	6	-	-	-	-			-		-		-	-	-		
						4.6	0.3	342	17.5	8.2	8.2	30.3	30.3	95.8	95.8	7.6	7.6	1.1	6	-	-	-	-	-			-		-		-	-	-		
					Bottom	8.2	0.3	350	17.5	17.5	8.2	8.2	30.4	30.4	95.8	95.8	7.6	7.6	1.6	4	-	-	-	-			-		-		-	-	-	-	
						8.2	0.2	348	17.5	8.2	8.2	30.4	30.4	95.8	95.8	7.6	7.6	1.6	3	-	-	-	-	-			-		-		-	-	-	-	
SR4A	Rainy	Moderate	08:35	9.4	Surface	1.0	0.1	199	17.1	17.1	8.2	8.2	31.9	31.9	97.6	97.4	7.8	7.8	5.4	6.2	3	3	-	-	817188	807822	-	-	-	-					
						1.0	0.1	206	17.1	8.2	8.2	31.9	31.9	97.1	97.1	7.7	5.5		4		-		-				-								
					Middle	4.7	0.0	210	17.1	17.1	8.2	8.2	31.9	31.9	97.6	97.3	7.8	7.7	6.1	3	-	-	-	-			-		-		-	-	-		
						4.7	0.0	216	17.1	8.2	8.2	31.9	31.9	97.0	97.0	7.7	7.7	6.2	3	-	-	-	-	-			-		-		-	-	-		
					Bottom	8.4	0.0	195	17.1	17.1	8.2	8.2	31.8	31.8	96.6	96.6	7.7	7.7	7.0	3	-	-	-	-			-		-		-	-	-	-	
						8.4	0.0	200	17.1	8.2	8.2	31.8	31.8	96.5	96.5	7.7	7.7	7.1	3	-	-	-	-	-			-		-		-	-	-	-	
SR8	Rainy	Moderate	09:10	3.6	Surface	1.0	-	-	18.2	18.2	8.2	8.2	31.4	31.4	97.7	97.7	7.6	7.6	1.1	1.7	3	4	-	-	820368	811628	-	-	-	-					
						1.0	-	-	18.2	8.2	8.2	31.4	31.4	97.7	97.7	7.6	1.2		3		-		-				-								
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	2.6	-	-	18.2	18.2	8.2	8.2	31.4	31.4	97.5	97.5	7.6	7.6	2.2	4	-	-	-	-			-		-		-	-	-	-	-
						2.6	-	-	18.2	8.2	8.2	31.4	31.4	97.5	97.5	7.6	7.6	2.4	4	-	-	-	-	-			-		-		-	-	-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 19 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Rainy	Rough	15:22	7.8	Surface	1.0	0.3	215	17.1	17.1	8.2	8.2	31.2	31.2	96.2	96.2	7.7	7.7	1.9	3.0	5	6	79	85	815598	804242	<0.2	<0.2	0.8	0.7
						1.0	0.3	210	17.1		8.2	8.2	31.2	31.2	96.2	96.2	7.7		1.9		6		79				<0.2		0.7	
					Middle	3.9	0.3	223	17.1	17.1	8.2	8.2	31.2	31.2	96.2	96.2	7.7	7.7	2.7	5	86	<0.2	<0.2	0.7						
						3.9	0.3	222	17.1		8.2	8.2	31.2	31.2	96.2	96.2	7.7		2.7	6	86	<0.2		0.7						
					Bottom	6.8	0.3	233	17.1	17.1	8.2	8.2	31.2	31.2	96.4	96.4	7.7	7.7	4.6	6	91	<0.2	<0.2	0.7						
						6.8	0.4	236	17.1		8.2	8.2	31.2	31.2	96.4	96.4	7.7		4.6	6	91	<0.2		0.7						
C2	Rainy	Rough	13:40	9.6	Surface	1.0	0.1	171	17.0	17.0	8.3	8.3	31.5	31.5	97.5	97.5	7.8	7.8	4.3	4.6	6	6	78	84	825678	806958	<0.2	<0.2	0.8	0.7
						1.0	0.1	164	17.0		8.3	8.3	31.5	31.5	97.5	97.5	7.8		4.4		5		79				<0.2		0.7	
					Middle	4.8	0.2	174	17.1	17.1	8.3	8.3	31.5	31.5	97.4	97.4	7.8	7.8	4.7	5	83	<0.2	<0.2	0.7						
						4.8	0.1	175	17.1		8.3	8.3	31.5	31.5	97.4	97.4	7.8		4.7	6	83	<0.2		0.7						
					Bottom	8.6	0.1	149	17.1	17.1	8.3	8.3	31.6	31.6	97.4	97.4	7.8	7.8	4.6	6	90	<0.2	<0.2	0.7						
						8.6	0.1	144	17.1		8.3	8.3	31.6	31.6	97.4	97.4	7.8		4.6	5	90	<0.2		0.7						
C3	Rainy	Moderate	14:05	12.0	Surface	1.0	0.2	67	17.8	17.7	8.2	8.2	32.0	32.0	103.3	103.3	8.1	8.1	3.0	4.1	7	6	52	74	822117	817819	<0.2	<0.2	0.7	0.7
						1.0	0.2	61	17.6		8.2	8.2	32.0	32.0	103.3	103.3	8.1		3.1		6		52				<0.2		0.7	
					Middle	6.0	0.3	69	17.6	17.6	8.2	8.2	31.9	31.9	103.5	103.6	8.1	8.1	4.1	6	82	<0.2	<0.2	0.6						
						6.0	0.2	63	17.6		8.2	8.2	31.9	31.9	103.6	103.6	8.1		4.2	5	82	<0.2		0.7						
					Bottom	11.0	0.3	61	17.6	17.7	8.2	8.2	31.9	31.9	103.8	103.9	8.2	8.2	5.1	5	87	<0.2	<0.2	0.7						
						11.0	0.2	59	17.8		8.2	8.2	31.9	31.9	103.9	103.9	8.2		5.0	5	87	<0.2		0.6						
IM1	Rainy	Rough	15:07	8.2	Surface	1.0	0.2	200	17.1	17.1	8.2	8.2	31.4	31.4	97.1	97.1	7.8	7.8	1.5	1.8	6	7	83	86	818353	806471	<0.2	<0.2	0.8	0.8
						1.0	0.2	197	17.1		8.2	8.2	31.4	31.4	97.1	97.1	7.8		1.5		8		83				<0.2		0.8	
					Middle	4.1	0.2	178	17.1	17.1	8.2	8.2	31.4	31.4	97.3	97.3	7.8	7.8	1.5	7	86	<0.2	<0.2	0.8						
						4.1	0.2	175	17.1		8.2	8.2	31.4	31.4	97.3	97.3	7.8		1.6	6	86	<0.2		0.8						
					Bottom	7.2	0.2	168	17.1	17.1	8.2	8.2	31.4	31.4	98.8	99.2	7.9	8.0	2.3	6	90	<0.2	<0.2	0.8						
						7.2	0.2	172	17.1		8.2	8.2	31.4	31.4	99.6	99.2	8.0		2.2	6	90	<0.2		0.7						
IM2	Rainy	Rough	14:52	8.5	Surface	1.0	0.2	196	16.9	16.9	8.3	8.3	31.8	31.8	98.8	98.8	7.9	7.9	3.2	3.4	5	6	83	86	819160	806225	<0.2	<0.2	0.7	0.8
						1.0	0.2	195	16.9		8.3	8.3	31.8	31.8	98.8	98.8	7.9		3.0		6		83				<0.2		0.7	
					Middle	4.3	0.1	170	16.9	16.9	8.3	8.3	31.8	31.8	98.6	98.6	7.9	7.9	3.4	5	87	<0.2	<0.2	0.7						
						4.3	0.1	172	16.9		8.3	8.3	31.8	31.8	98.6	98.6	7.9		3.4	6	87	<0.2		0.8						
					Bottom	7.5	0.2	194	16.9	16.9	8.3	8.3	31.8	31.8	98.8	98.9	7.9	7.9	3.7	5	91	<0.2	<0.2	0.8						
						7.5	0.2	192	16.9		8.3	8.3	31.8	31.8	98.9	98.9	7.9		3.6	6	87	<0.2		0.8						
IM7	Rainy	Rough	14:21	8.4	Surface	1.0	0.1	103	16.9	16.9	8.3	8.3	31.8	31.8	98.4	98.4	7.9	7.9	4.1	4.2	5	6	86	85	821355	806818	<0.2	<0.2	0.7	0.7
						1.0	0.1	106	16.9		8.3	8.3	31.8	31.8	98.4	98.4	7.9		4.1		6		86				<0.2		0.7	
					Middle	4.2	0.1	95	17.0	17.0	8.3	8.3	31.8	31.8	97.9	97.9	7.8	7.8	4.2	6	83	<0.2	<0.2	0.7						
						4.2	0.2	97	17.0		8.3	8.3	31.8	31.8	97.9	97.9	7.8		4.2	6	83	<0.2		0.7						
					Bottom	7.4	0.1	105	17.0	17.0	8.3	8.3	31.8	31.8	98.0	98.0	7.8	7.8	4.3	5	86	<0.2	<0.2	0.7						
						7.4	0.2	102	17.0		8.3	8.3	31.8	31.8	98.0	98.0	7.8		4.3	6	86	<0.2		0.7						

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 19 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)					
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA
IM10	Rainy	Moderate	13:06	8.4	Surface	1.0	0.1	9	17.8	17.8	8.2	8.2	31.9	31.9	103.9	103.9	8.2	8.2	4.1	4.7	7	7	52	77	822226	809830	<0.2	<0.2	0.9	0.7				
						1.0	0.1	9	17.8	8.2	31.9	103.9	8.2	4.1	7	52	<0.2		0.7															
					Middle	4.2	0.1	20	17.8	17.8	8.2	8.2	31.9	31.9	104.1	104.2	8.2	5.0	7	87	<0.2	0.6												
						4.2	0.1	13	17.8	8.2	8.2	31.9	31.9	104.2	8.2	5.0	6	88	<0.2	0.7														
					Bottom	7.4	0.0	31	17.8	8.2	8.2	31.9	31.9	104.3	8.2	4.9	8	90	<0.2	0.7														
						7.4	0.1	26	17.8	8.2	8.2	31.9	31.9	104.3	8.2	4.9	7	90	<0.2	0.7														
IM11	Rainy	Moderate	13:10	8.2	Surface	1.0	0.1	44	17.8	17.8	8.2	8.2	32.0	32.0	102.5	102.5	8.1	8.1	3.8	4.5	5	7	63	75	821484	810529	<0.2	<0.2	0.7	0.7				
						1.0	0.1	44	17.8	8.2	32.0	102.4	8.1	3.9	6	63	<0.2		0.8															
					Middle	4.1	0.1	69	17.7	17.7	8.2	8.2	32.0	32.0	102.3	102.3	8.0	4.1	8	78	<0.2	0.8												
						4.1	0.1	75	17.7	8.2	8.2	32.0	32.0	102.2	8.0	4.2	7	79	<0.2	0.6														
					Bottom	7.2	0.1	64	17.8	17.8	8.2	8.2	31.9	31.9	102.1	102.2	8.0	5.4	7	85	<0.2	0.7												
						7.2	0.1	66	17.8	8.2	8.2	31.9	31.9	102.2	8.0	5.5	7	84	<0.2	0.7														
IM12	Rainy	Moderate	13:17	8.6	Surface	1.0	0.1	83	17.7	17.7	8.2	8.2	32.0	32.0	103.0	103.0	8.1	8.1	1.4	2.5	7	7	48	73	821171	811540	<0.2	<0.2	0.8	0.8				
						1.0	0.1	80	17.7	8.2	32.0	103.0	8.1	1.4	6	49	<0.2		0.7															
					Middle	4.3	0.1	87	17.7	17.7	8.2	8.2	32.0	32.0	102.9	102.9	8.1	2.6	7	83	<0.2	0.8												
						4.3	0.2	93	17.7	8.2	8.2	32.0	32.0	102.9	8.1	2.5	6	83	<0.2	0.8														
					Bottom	7.6	0.1	108	17.7	17.7	8.2	8.2	32.0	32.0	102.8	102.8	8.1	3.7	7	87	<0.2	0.8												
						7.6	0.1	103	17.7	8.2	8.2	32.0	32.0	102.8	8.1	3.7	8	88	<0.2	0.7														
SR1A	Rainy	Moderate	13:34	5.0	Surface	1.0	0.0	35	17.6	17.7	8.2	8.2	32.0	32.0	102.9	102.9	8.1	8.1	3.5	3.9	6	6	-	-	819972	812654	-	-	-	-				
						1.0	0.0	29	17.8	8.2	32.0	102.9	8.1	3.5	6	-	-		-		-													
					Middle	2.5	0.0	28	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-
						2.5	0.0	24	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	4.0	0.0	42	17.8	17.8	8.2	8.2	32.0	31.9	102.8	102.8	8.1	4.4	7	-	-	-	-	-			-		-		-	-	-	-
						4.0	0.0	44	17.8	8.2	8.2	31.9	31.9	102.8	8.1	4.4	6	-	-	-	-	-	-	-			-		-		-	-	-	
SR2	Rainy	Moderate	13:44	5.2	Surface	1.0	0.1	60	17.8	17.7	8.2	8.2	32.0	32.0	103.1	103.1	8.1	8.1	1.2	1.6	6	6	69	78	821476	814183	<0.2	<0.2	0.7	0.7				
						1.0	0.1	53	17.6	8.2	32.0	103.1	8.1	1.2	4	69	<0.2		0.7															
					Middle	-	0.2	58	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-
						-	0.2	50	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
					Bottom	4.2	0.2	55	17.6	17.6	8.2	8.2	32.0	32.0	103.1	103.1	8.1	2.1	7	86	<0.2	0.7												
						4.2	0.2	56	17.6	8.2	8.2	32.0	32.0	103.1	8.1	2.0	6	86	<0.2	0.8														
SR3	Rainy	Rough	14:12	7.9	Surface	1.0	0.2	141	17.0	17.0	8.3	8.3	31.6	31.6	98.2	98.2	7.9	7.9	5.8	5.3	8	8	-	-	822141	807591	-	-	-	-				
						1.0	0.1	134	17.0	8.3	31.6	98.2	7.9	5.9	6	-	-		-		-													
					Middle	4.0	0.2	136	17.0	17.0	8.3	8.3	31.6	31.6	98.1	98.1	7.8	4.5	7	-	-	-	-	-			-		-		-	-	-	
						4.0	0.2	134	17.0	8.3	31.6	98.1	7.8	4.6	8	-	-	-	-	-	-	-	-	-			-		-		-	-		
					Bottom	6.9	0.2	134	17.0	17.0	8.3	8.3	31.7	31.7	98.1	98.1	7.8	5.4	9	-	-	-	-	-			-		-		-	-	-	-
						6.9	0.2	127	17.0	8.3	31.7	98.1	7.8	5.4	7	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
SR4A	Rainy	Rough	15:46	10.3	Surface	1.0	0.0	16	17.2	17.2	8.2	8.2	31.6	31.6	94.0	94.0	7.5	7.5	3.8	4.8	9	8	-	-	817195	807815	-	-	-	-				
						1.0	0.0	16	17.2	8.2	31.6	93.9	7.5	3.8	7	-	-		-		-													
					Middle	5.2	0.0	37	17.2	17.2	8.2	8.2	31.7	31.7	93.7	93.8	7.5	4.3	8	-	-	-	-	-			-		-		-	-	-	
						5.2	0.1	41	17.2	8.2	31.7	93.8	7.5	4.3	7	-	-	-	-	-	-	-	-	-			-		-		-	-		
					Bottom	9.3	0.0	12	17.2	17.2	8.2	8.2	31.7	31.7	94.8	94.8	7.5	6.2	8	-	-	-	-	-			-		-		-	-	-	
						9.3	0.0	7	17.2	8.2	31.7	94.8	7.5	6.3	8	-	-	-	-	-	-	-	-	-			-		-		-	-		
SR8	Rainy	Moderate	13:21	4.8	Surface	1.0	-	-	17.8	17.8	8.2	8.2	31.9	31.9	103.7	103.7	8.1	8.1	1.6	2.0	7	7	-	-	820388	811645	-	-	-	-				
						1.0	-	-	17.8	8.2	31.9	103.7	8.1	1.5	9	-	-		-		-													
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-		
					Bottom	3.8	-	-	17.7	17.7	8.2	8.2	32.0	32.0	103.7	103.6	8.2	2.4	-	-	-	-	-	-			-		-		-	-	-	-
						3.8	-	-	17.7	8.2	32.0	32.0	8.2	2.4	6	-	-	-	-	-	-	-	-	-			-		-		-	-		

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 19 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Rainy	Rough	08:22	7.1	Surface	1.0	0.2	33	16.9	16.9	8.3	8.3	32.2	32.2	99.4	99.4	7.9		6.2		7		82		815613	804245	<0.2		0.7	
						1.0	0.1	30	16.9		8.3		32.2		99.4		7.9		6.3		8		83				<0.2		0.7	
					Middle	3.6	0.3	30	16.9	16.9	8.3	8.3	32.2	32.2	99.4	99.4	7.9	7.9	3.3	5.0	7	7	86	86			<0.2	<0.2	0.7	0.7
						3.6	0.2	30	16.9		8.3		32.2		99.4		7.9		3.3		6		86				<0.2		0.7	
					Bottom	6.1	0.2	8	16.9	16.9	8.3	8.3	32.1	32.1	99.4	99.4	7.9	7.9	5.6		5		90				<0.2		0.7	
						6.1	0.2	8	16.9		8.3		32.1		99.4		7.9		5.6		6		90				<0.2		0.7	
					Surface	1.0	0.4	359	17.1		8.3	8.3	31.5	31.5	97.5	97.5	7.8		5.7		7		83				<0.2		0.6	
						1.0	0.4	0	17.1	17.1	8.3	8.3	31.5	31.5	97.5	97.5	7.8	7.8	5.7		8		83				<0.2		0.7	
C2	Rainy	Rough	09:54	8.4	Surface	4.2	0.4	7	17.1		8.3	8.3	31.5	31.5	97.4	97.4	7.8	7.8	6.5	6.4	7	7	86	86	825659	806961	<0.2	<0.2	0.7	0.7
						4.2	0.4	11	17.1	17.1	8.3	8.3	31.5	31.5	97.4	97.4	7.8		6.4		5		86				<0.2	<0.2	0.7	
					Middle	7.4	0.4	346	17.1		8.3	8.3	31.5	31.5	97.4	97.4	7.8	7.8	7.2		6		90				<0.2		0.7	
						7.4	0.3	346	17.1	17.1	8.3	8.3	31.5	31.5	97.4	97.4	7.8	7.8	7.2		8		90				<0.2		0.6	
					Surface	1.0	0.5	276	17.6	17.6	8.0	8.0	31.8	31.8	103.4	103.4	8.1		2.3		4		44				<0.2		0.7	
						1.0	0.5	282	17.6		8.0		31.8		103.3		8.1	8.1	2.3		4		44				<0.2		0.8	
					Middle	6.0	0.4	272	17.8	17.8	8.0	8.0	31.8	31.8	103.3	103.3	8.1		3.3	3.2	6	5	86	86			<0.2	<0.2	0.7	0.7
						6.0	0.4	266	17.8		8.0		31.8		103.2		8.1		3.3		5		86				<0.2		0.7	
C3	Rainy	Moderate	09:23	12.0	Surface	11.0	0.5	253	17.8		8.0	8.0	31.8	31.8	103.1	103.1	8.1	8.1	4.1		5		87		822090	817783	<0.2		0.7	
						11.0	0.4	249	17.8	17.8	8.0	8.0	31.8	31.8	103.1	103.1	8.1	8.1	4.1		5		87				<0.2		0.7	
					Middle	6.2	0.1	359	17.0		8.3	8.3	31.6	31.6	98.4	98.4	7.9	7.9	5.1		6		91				<0.2		0.7	
						6.2	0.1	5	17.0	17.0	8.3	8.3	31.6	31.6	98.4	98.4	7.9	7.9	5.2		5		91				<0.2		0.7	
					Bottom	1.0	0.2	6	17.0	17.0	8.3	8.3	31.6	31.6	97.9	97.9	7.8	7.8	3.9		4		82				<0.2		0.7	
						1.0	0.1	6	17.0		8.3		31.6		97.9		7.8		3.9		5		82				<0.2		0.7	
					Surface	3.6	0.1	4	17.0	17.0	8.3	8.3	31.6	31.6	98.0	98.0	7.8	7.8	5.0	4.7	5	5	86	86			<0.2	<0.2	0.7	0.7
						3.6	0.1	6	17.0		8.3		31.6		98.0		7.8		5.0		4		87				<0.2		0.6	
IM1	Rainy	Rough	08:47	7.2	Surface	6.2	0.1	359	17.0		8.3	8.3	31.6	31.6	98.4	98.4	7.9	7.9	5.1		6		91		818368	806450	<0.2		0.7	
						6.2	0.1	5	17.0	17.0	8.3	8.3	31.6	31.6	98.4	98.4	7.9	7.9	5.2		5		91				<0.2		0.7	
					Middle	1.0	0.2	348	17.1	17.1	8.3	8.3	31.5	31.5	97.8	97.8	7.8	7.8	4.1		4		83				<0.2		0.7	
						1.0	0.2	346	17.1		8.3		31.5		97.8		7.8		4.1		4		83				<0.2		0.6	
					Middle	4.2	0.1	347	17.1	17.1	8.3	8.3	31.5	31.5	97.8	97.8	7.8	7.8	4.2	4.7	5	4	87	87			<0.2	<0.2	0.7	0.7
						4.2	0.1	348	17.1		8.3		31.5		97.8		7.8		4.3		4		87				<0.2		0.7	
					Bottom	7.4	0.1	342	17.1		8.3	8.3	31.6	31.6	98.0	98.0	7.8	7.8	5.6		5		90				<0.2		0.7	
						7.4	0.1	339	17.1	17.1	8.3	8.3	31.6	31.6	98.0	98.0	7.8	7.8	5.6		4		90				<0.2		0.6	
IM2	Rainy	Rough	08:53	8.4	Surface	1.0	0.2	328	17.1	17.1	8.3	8.3	31.4	31.4	98.1	98.1	7.8	7.8	6.2		6		82		819196	806242	<0.2		0.6	
						1.0	0.2	330	17.1		8.3		31.4		98.1		7.8		6.2		4		82				<0.2		0.7	
					Middle	4.1	0.1	315	17.1	17.1	8.3	8.3	31.4	31.4	98.0	98.0	7.8	7.8	8.3		5	6	87	87			<0.2	<0.2	0.6	0.6
						4.1	0.2	314	17.1		8.3		31.4		98.0		7.8		8.3		6		87				<0.2		0.7	
					Bottom	7.2	0.2	354	17.1		8.3	8.3	31.4	31.4	98.3	98.3	7.8	7.9	4.4		7		90				<0.2		0.6	
						7.2	0.2	355	17.1	17.1	8.3	8.3	31.4	31.4	98.3	98.3	7.9	7.9	4.5		6		90				<0.2		0.6	
					Surface	1.0	0.2	328	17.1	17.1	8.3	8.3	31.4	31.4	98.1	98.1	7.8	7.8	6.2		6		82		821334	806826	<0.2		0.6	
						1.0	0.2	330	17.1		8.3		31.4		98.1		7.8		6.2		4		82				<0.2		0.7	
IM7	Rainy	Rough	09:20	8.2	Surface	4.1	0.1	315	17.1	17.1	8.3	8.3	31.4	31.4	98.0	98.0	7.8	7.8	8.3		5	6	87	87			<0.2	<0.2	0.6	0.6
						4.1	0.2	314	17.1		8.3		31.4		98.0		7.8		8.3		6		87				<0.2		0.7	
					Middle	7.2	0.2	354	17.1		8.3	8.3	31.4	31.4	98.3	98.3	7.8	7.9	4.4		7		90				<0.2		0.6	
						7.2	0.2	355	17.1	17.1	8.3	8.3	31.4	31.4	98.3	98.3	7.9	7.9	4.5		6		90				<0.2		0.6	
					Bottom	1.0	0.2	328	17.1	17.1	8.3	8.3	31.4	31.4	98.1	98.1	7.8	7.8	6.2		6		82				<0.2		0.6	
						1.0	0.2	330	17.1		8.3		31.4		98.1		7.8		6.2		4		82				<0.2		0.7	
					Surface	4.1	0.1	315	17.1	17.1	8.3	8.3	31.4	31.4	98.0	98.0	7.8	7.8	8.3		5	6	87	87			<0.2	<0.2	0.6	0.

Expansion of Hong Kong International Airport into a Three-Runway System
Water Quality Monitoring

Water Quality Monitoring Results on 19 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)					
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA		
IM10	Rainy	Moderate	10:09	8.0	Surface	1.0	0.3	290	17.8	17.8	8.2	8.2	31.9	31.9	103.8	103.9	8.2	8.2	4.0	5.2	5	6	49	73	822225	809847	<0.2	<0.2	0.7	0.7				
						1.0	0.3	283	17.8	17.8	8.2	8.2	31.9	103.9	8.2	4.1	48		<0.2		0.8													
					Middle	4.0	0.3	282	17.8	17.8	8.2	8.2	31.9	103.9	8.2	5.1	83	<0.2	0.9															
						4.0	0.4	278	17.8	17.8	8.2	8.2	31.9	103.9	8.2	5.1	83	<0.2	0.7															
					Bottom	7.0	0.3	306	17.8	17.8	8.2	8.1	31.8	31.8	104.2	104.3	8.2	8.2	6.5	9	86	<0.2	0.6											
						7.0	0.3	310	17.8	17.8	8.1	8.1	31.8	104.3	8.2	6.5	8		86	<0.2	0.7													
IM11	Rainy	Moderate	10:02	7.6	Surface	1.0	0.4	277	17.8	17.8	8.1	8.1	32.0	32.0	103.9	103.9	8.2	8.2	3.3	4.2	6	5	48	821509	810523	<0.2	<0.2	0.7	0.8					
						1.0	0.4	281	17.8	17.8	8.1	8.1	32.0	103.8	8.2	3.4	48		<0.2		0.7													
					Middle	3.8	0.4	299	17.8	17.8	8.1	8.1	32.0	103.8	8.2	4.0	86	<0.2	0.7															
						3.8	0.4	298	17.8	17.8	8.1	8.1	32.0	103.7	8.2	4.1	86	<0.2	0.9															
					Bottom	6.6	0.4	287	17.8	17.8	8.1	8.1	31.9	103.7	8.1	8.2	5.2	5	90	<0.2	0.9													
						6.6	0.3	282	17.8	17.8	8.1	8.1	31.9	103.6	8.2		5.2	4	90	<0.2	0.8													
IM12	Rainy	Moderate	09:57	8.4	Surface	1.0	0.4	282	17.8	17.8	8.1	8.1	31.9	31.9	103.3	103.3	8.1	8.1	3.5	4.4	4	4	45	821145	811522	<0.2	<0.2	0.7	0.8					
						1.0	0.4	286	17.8	17.8	8.1	8.1	31.9	103.3	8.1	3.5	5		45		<0.2		0.6											
					Middle	4.2	0.5	264	17.8	17.8	8.1	8.1	31.9	103.3	8.1	4.1	4	86	<0.2	0.8														
						4.2	0.5	263	17.8	17.8	8.1	8.1	31.9	103.3	8.1	4.2	3	86	<0.2	0.9														
					Bottom	7.4	0.5	261	17.8	17.8	8.1	8.1	31.9	103.3	8.1	8.1	5.7	5	87	<0.2	0.8													
						7.4	0.5	262	17.8	17.8	8.1	8.1	31.9	103.3	8.1		5.7	5	87	<0.2	0.8													
SR1A	Rainy	Moderate	09:37	5.0	Surface	1.0	0.0	204	17.7	17.7	8.1	8.1	31.9	31.9	100.6	100.6	7.9	7.9	2.0	2.4	4	5	-	819971	812665	-	-	-	-					
						1.0	0.0	207	17.7	-	-	-	-	-	7.9	1.9	4		-		-		-											
					Middle	2.5	0.0	201	-	-	-	-	-	-	-	-	-	-	-	-	5	-	-			-		-		-	-	-		
						2.5	0.0	199	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.0	0.0	187	17.7	17.7	8.1	8.1	31.9	100.7	7.9	8.0	2.9	5	-	-	-	-	-			-		-		-	-	-		
						4.0	0.1	180	17.7	17.7	8.1	8.1	31.9	101.1	8.1		2.9	7	-	-	-	-	-			-		-		-	-	-		
SR2	Rainy	Moderate	09:23	5.0	Surface	1.0	0.1	224	17.8	17.8	8.0	8.0	31.9	31.9	103.4	103.4	8.1	8.1	4.0	4.8	6	5	43	821454	814164	<0.2	<0.2	0.7	0.7					
						1.0	0.2	216	17.8	17.8	8.0	8.0	31.9	103.4	8.1	4.1	5		43		<0.2		0.6											
					Middle	-	0.1	238	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-	-	
						-	0.1	235	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.0	0.1	248	17.6	17.6	8.0	8.0	31.9	103.5	8.1	8.1	5.7	4	87	<0.2	0.7													
						4.0	0.1	251	17.6	17.6	8.0	8.0	31.9	103.6	8.1		5.6	5	87	<0.2	0.6													
SR3	Rainy	Rough	09:27	7.1	Surface	1.0	0.3	333	17.1	17.1	8.3	8.3	31.4	31.4	97.8	97.8	7.8	7.8	5.2	6.6	8	9	-	822142	807589	-	-	-	-					
						1.0	0.3	336	17.1	17.1	8.3	8.3	31.4	97.8	7.8	5.2	10		-		-													
					Middle	3.6	0.3	351	17.1	17.1	8.3	8.3	31.4	97.7	7.8	7.3	7	-	-	-	-													
						3.6	0.2	354	17.1	17.1	8.3	8.3	31.4	97.7	7.8	7.4	9	-	-	-	-													
					Bottom	6.1	0.3	316	17.1	17.1	8.3	8.3	31.4	97.8	7.8	7.2	11	-	-	-	-													
						6.1	0.3	316	17.1	17.1	8.3	8.3	31.4	97.9	7.8	7.2	9	-	-	-	-													
SR4A	Rainy	Moderate	07:57	10.2	Surface	1.0	0.0	159	17.0	17.0	8.1	8.1	31.9	31.9	98.4	98.4	7.9	7.9	2.6	3.1	6	5	-	817169	807806	-	-	-	-					
						1.0	0.0	157	17.0	17.0	8.1	8.1	31.9	98.4	7.9	2.5	4		-		-													
					Middle	5.1	0.1	160	17.0	17.0	8.1	8.1	31.9	98.1	7.8	2.7	5	-	-	-	-													
						5.1	0.1	161	17.0	17.0	8.1	8.1	31.9	98.1	7.8	2.8	5	-	-	-	-													
					Bottom	9.2	0.0	177	17.0	17.0	8.1	8.1	31.9	97.7	7.8	4.0	4	-	-	-	-													
						9.2	0.0	174	17.0	17.0	8.1	8.1	31.9	97.7	7.8	4.1	3	-	-	-	-													
SR8	Rainy	Moderate	09:54	5.0	Surface	1.0	-	-	17.8	17.8	8.2	8.2	31.9	31.9	102.9	102.9	8.1	8.1	3.3	3.7	5	4	-	820381	811605	-	-	-	-					
						1.0	-	-	17.8	17.8	8.2	8.2	31.9	102.9	8.1	3.3	4		-		-													
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-		
					Bottom	4.0	-	-	17.7	17.7	8.2	8.2	31.9	31.9	102.8	102.8	8.1	8.1	4.1	4	-	-	-			-		-		-	-	-	-	-
						4.0	-	-	17.7	17.7	8.2	8.2	31.9	102.8	8.1	4.1	4		-	-	-	-	-			-		-		-	-	-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 22 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)									
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA						
C1	Rainy	Moderate	16:31	8.2	Surface	1.0	0.2	214	15.3	15.3	8.2	8.2	31.2	31.2	104.6	104.6	8.7	8.6	5.1	8.0	4	5	82	87	815636	804241	<0.2	0.7	0.7									
						1.0	0.2	212	15.3	15.3	8.2	8.2	31.2	104.5	8.6	5.1	5		83		<0.2		0.6															
					Middle	4.1	0.3	223	15.5	15.5	8.2	8.2	32.3	103.6	103.6	8.5	9.1		5		88		<0.2				0.7											
						4.1	0.2	224	15.5	15.5	8.2	8.2	32.3	103.6	103.6	8.5	9.1		5		88		<0.2				0.7											
					Bottom	7.2	0.3	234	15.5	15.5	8.2	8.2	32.5	104.5	104.8	8.6	9.6	5	90	<0.2	0.7																	
						7.2	0.2	237	15.5	15.5	8.2	8.2	32.5	104.8	105.1	8.6	10.0	5	91	<0.2	0.6																	
						C2	Rainy	Moderate	15:07	10.2	Surface	1.0	0.2	168	15.5	15.5	8.2	8.2	31.0	31.0	102.4	102.3	8.5	8.4			3.6	3.8		5	4	82	86	825688	806937	<0.2	0.8	0.8
												1.0	0.2	170	15.5	15.5	8.2	8.2	31.0	102.2	8.4	3.7	4				82			<0.2		0.8						
Middle	5.1	0.2	187	15.8	15.8						8.2	8.2	31.6	101.7	101.6	8.3	4.0	3	86	<0.2	0.9																	
	5.1	0.2	190	15.8	15.8						8.2	8.2	31.6	101.5	101.6	8.3	4.0	4	86	<0.2	0.8																	
Bottom	9.2	0.2	183	16.0	15.9						8.2	8.2	31.8	104.3	104.3	8.5	3.7	4	91	<0.2	0.8																	
	9.2	0.2	189	15.8	15.9						8.2	8.2	31.6	104.3	104.3	8.5	3.8	4	91	<0.2	0.8																	
	C3	Rainy	Rough	17:07	10.5						Surface	1.0	0.4	91	15.6	15.6	8.3	8.3	31.6	31.6	93.6	93.6	7.7	7.7	1.7	1.7	5	3	82	86	822116	817824	<0.2			0.6	0.6	
												1.0	0.4	90	15.6	15.6	8.3	8.3	31.6	93.6	7.7	1.7	5		82		<0.2		0.7									
Middle						5.3	0.4	76	15.6	15.6	8.3	8.3	31.7	92.7	92.7	7.6	1.4	3	87	<0.2	0.6																	
						5.3	0.3	70	15.6	15.6	8.3	8.3	31.7	92.7	92.7	7.6	1.4	3	87	<0.2	0.7																	
Bottom						9.5	0.4	80	15.7	15.7	8.3	8.3	31.8	93.2	93.3	7.6	2.1	2	90	<0.2	0.5																	
						9.5	0.4	85	15.7	15.7	8.3	8.3	31.8	93.4	93.3	7.7	2.0	2	90	<0.2	0.6																	
						IM1	Rainy	Moderate	16:10	6.1	Surface	1.0	0.1	178	15.1	15.2	8.2	8.2	31.3	31.5	105.1	104.7	8.7	8.6	4.2	4.9	4	5	82	87			818328	806445	<0.2	0.7		0.7
												1.0	0.1	176	15.2	15.2	8.2	8.2	31.6	104.3	8.6	4.2	5		82		<0.2		0.7									
Middle	3.1	0.1	189	15.3	15.3						8.2	8.2	32.1	103.9	103.7	8.6	4.4	5	87	<0.2	0.8																	
	3.1	0.1	188	15.3	15.3						8.2	8.2	32.2	103.5	103.5	8.5	4.9	5	87	<0.2	0.7																	
Bottom	5.1	0.1	171	15.3	15.3						8.2	8.2	32.4	104.2	104.8	8.6	6.3	6	91	<0.2	0.7																	
	5.1	0.1	174	15.3	15.3						8.2	8.2	32.2	105.3	104.8	8.7	5.6	7	91	<0.2	0.7																	
	IM2	Rainy	Moderate	16:04	6.5						Surface	1.0	0.1	182	15.2	15.2	8.2	8.2	31.7	31.8	104.4	104.4	8.6	8.6	4.8	5.0	9	8	82	87	819188	806255			<0.2	0.6	0.6	
												1.0	0.1	175	15.2	15.2	8.2	8.2	31.8	104.3	8.6	4.8	8		84		<0.2		0.6									
Middle						3.3	0.2	179	15.2	15.2	8.2	8.2	32.1	104.2	104.2	8.6	5.1	7	87	<0.2	0.6																	
						3.3	0.2	175	15.2	15.2	8.2	8.2	32.1	104.2	104.2	8.6	5.0	8	88	<0.2	0.7																	
Bottom						5.5	0.1	167	15.2	15.2	8.3	8.3	32.2	103.8	103.9	8.6	5.1	7	92	<0.2	0.5																	
						5.5	0.1	166	15.2	15.2	8.3	8.3	32.2	103.9	103.9	8.6	5.1	7	91	<0.2	0.6																	
						IM7	Rainy	Moderate	15:40	7.0	Surface	1.0	0.1	117	15.3	15.3	8.2	8.2	32.0	32.0	103.0	103.0	8.5	8.5	4.5	4.4	5	7	83	88			821368	806854	<0.2	0.5		0.5
												1.0	0.1	124	15.3	15.3	8.2	8.2	32.0	102.9	8.5	4.4	6		83		<0.2		0.6									
Middle	3.5	0.1	127	15.3	15.3						8.2	8.2	32.1	102.9	102.9	8.5	4.3	7	88	<0.2	0.6																	
	3.5	0.2	119	15.3	15.3						8.2	8.2	32.1	102.9	102.9	8.5	4.3	7	88	<0.2	0.4																	
Bottom	6.0	0.1	144	15.3	15.3						8.2	8.2	32.0	103.4	103.8	8.5	4.4	8	92	<0.2	0.5																	
	6.0	0.2	148	15.3	15.3						8.2	8.2	32.1	104.2	103.8	8.6	4.6	8	92	<0.2	0.6																	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**</

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 22 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)													
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA										
IM10	Rainy	Rough	15:14	8.2	Surface	1.0	0.2	82	15.4	15.4	8.2	8.2	31.3	31.3	93.2	93.2	7.7	7.7	4.3	4.3	4	5	83	86	822247	809819	<0.2	<0.2	0.6	0.6												
						1.0	0.1	78	15.4		8.2		31.3		93.2		7.7												4.3			4		83		<0.2		0.6				
					Middle	4.1	0.2	83	15.4	15.4	8.2	8.2	31.3	31.3	93.0	93.1	7.7										7.7		3.3		4.3	5	86	86	<0.2	<0.2	0.5					
						4.1	0.1	84	15.4		8.2		31.3		93.1		7.7												3.3			4		90		<0.2		0.6				
					Bottom	7.2	0.2	96	15.4		8.2	8.2	31.3	31.3	93.4		7.7										7.7		5.3			7		90		<0.2		0.6				
						7.2	0.2	88	15.4	15.4	8.2	8.2	31.3	31.3	93.5	93.5	7.7										7.7		5.3			8		90		<0.2		0.6				
IM11	Rainy	Rough	15:23	8.1	Surface	1.0	0.3	84	15.5	15.5	8.2	8.2	31.4	31.4	93.4	93.4	7.7	7.7	1.4	1.4	6	5	78	87	821494	810547	<0.2	<0.2	0.6	0.7												
						1.0	0.3	82	15.5		8.2		31.4		93.4		7.7										7.7		1.4			7		79		<0.2		0.6				
					Middle	4.1	0.3	101	15.5	15.5	8.2	8.2	31.4	31.4	93.4	93.4	7.7										7.7		2.2		2.3	4	5	87	87	<0.2	<0.2	0.7				
						4.1	0.3	106	15.5		8.2		31.4		93.4		7.7												2.2			5		87		<0.2		0.7				
					Bottom	7.1	0.3	108	15.5	15.5	8.3	8.3	31.4	31.4	93.8	93.8	7.7										7.7		3.3			4		91		<0.2		0.6				
						7.1	0.3	111	15.5		8.3		31.4		93.8		7.7										7.7		3.3			4		91		<0.2		0.8				
IM12	Rainy	Rough	15:31	9.4	Surface	1.0	0.3	81	15.6	15.6	8.2	8.2	31.5	31.5	93.4	93.4	7.7	7.7	1.2	1.2	3	4	79	83	821159	811523	<0.2	<0.2	0.6	0.7												
						1.0	0.3	82	15.6		8.2		31.5		93.3		7.7										7.7		1.2			3		79		<0.2		0.7				
					Middle	4.7	0.3	69	15.6	15.6	8.2	8.2	31.5	31.5	93.2	93.3	7.7										7.7		2.2		4.4	4	4	83	83	<0.2	<0.2	0.7				
						4.7	0.3	66	15.6		8.2		31.5		93.3		7.7												2.2			4		83		<0.2		0.7				
					Bottom	8.4	0.3	66	15.6	15.6	8.3	8.3	31.5	31.5	93.9	94.0	7.7										7.7		10.0			5		87		<0.2		0.6				
						8.4	0.3	68	15.6		8.3		31.5		94.0		7.7										7.7		10.0			6		87		<0.2		0.6				
SR1A	Rainy	Moderate	16:00	4.8	Surface	1.0	0.0	82	15.1	15.1	8.3	8.3	30.6	30.6	92.5	92.5	7.7	7.7	3.3	3.3	4	5	-	-	819980	812664	-	-	-	-												
						1.0	0.1	80	15.1		8.3		30.7		92.5		7.7										7.7		3.3			4		-	-	-		-				
					Middle	2.4	0.0	81	-	-	-	-	-	-	-	-	-										-		-		4.0	-	-	-	-	-	-	-	-	-	-	-
						2.4	0.0	79	-		-		-		-		-												-			-		-	-	-	-	-	-	-	-	
					Bottom	3.8	-	96	15.1	15.1	8.3	8.3	30.7	30.7	92.3	92.4	7.7										7.7		4.7			6		-	-	-	-	-	-	-	-	-
						3.8	-	95	15.1		8.3		30.7		92.4		7.7										7.7		4.7			6		-	-	-	-	-	-	-	-	-
SR2	Rainy	Moderate	16:16	5.1	Surface	1.0	0.2	65	15.6	15.6	8.3	8.3	31.6	31.6	93.7	93.8	7.7	7.7	1.9	1.9	4	4	83	85	821452	814157	<0.2	<0.2	0.6	0.6												
						1.0	0.2	62	15.6		8.3		31.6		93.8		7.7										7.7		1.9			4		83		<0.2		0.5				
					Middle	-	0.2	49	-	-	-	-	-	-	-	-	-										-		-		2.3	-	-	-	-	-	-	-	-	-	-	-
						-	0.3	50	-		-		-		-		-												-			-		-	-	-	-	-	-	-	-	
					Bottom	4.1	0.2	32	15.6	15.6	8.3	8.3	31.7	31.7	95.5	95.8	7.8										7.9		2.6			4		87		<0.2		0.7				
						4.1	0.3	27	15.6		8.3		31.7		96.0		7.9												2.7			4		88		<0.2		0.7				
SR3	Rainy	Moderate	15:32	8.3	Surface	1.0	0.2	137	15.3	15.3	8.2	8.2	31.7	31.7	103.0	103.0	8.5	8.5	5.7	5.7	7	7	-	-	822138	807573	-	-	-	-												
						1.0	0.2	135	15.3		8.2		31.7		103.0		8.5										8.5		5.8			7		-	-	-		-				
					Middle	4.2	0.2	151	15.3	15.3	8.2	8.2	31.8	31.8	102.9	102.9	8.5												6.2		6.0	6	7	-	-	-	-	-	-	-	-	
						4.2	0.2	150	15.3		8.2		31.8		102.9		8.5												6.2			7		-	-	-	-	-	-	-	-	
					Bottom	7.3	0.2	136	15.3		8.2	8.2	31.9	31.9	103.0	103.1	8.5										8.5		6.1			6		-	-	-	-	-	-	-	-	
						7.3	0.2	129	15.3	15.3	8.2		31.9	31.9	103.1		8.5												6.1			6		-	-	-	-	-	-	-	-	
SR4A	Rainy	Calm	16:52	8.3	Surface	1.0	0.0	71	15.1	15.1	8.2	8.2	31.8	31.8	104.9	104.9	8.7	8.7	4.5	4.6	5	6	-	-	817199	807788	-	-	-	-												
						1.0	0.0	68	15.1		8.2		31.8		104.8		8.7										8.7		4.6			5		-	-	-		-				
					Middle	4.2	0.1	70	15.1	15.1	8.2	8.2	31.9	31.9	104.6	104.6	8.7												4.6		4.7	5	6	-	-	-	-	-	-	-	-	
						4.2	0.1	75	15.1		8.2		31.9		104.5		8.6												4.6			6		-	-	-	-	-	-	-		
					Bottom	7.3	0.0	77	15.1	15.1	8.2	8.2	32.2	32.2	104.2	104.2	8.6										8.6		5.0			6		-	-	-	-	-	-	-	-	
						7.3	0.0	70	15.1		8.2		32.2		104.2		8.6												5.1			6		-	-	-	-	-	-	-	-	
SR8	Rainy	Moderate	15:37	4.3	Surface	1.0	-	-	15.3	15.3	8.3	8.3	30.8	30.8	94.7	94.7	7.9	7.9	2.0	2.0	3	4	-	-	820379	811608	-	-	-	-												
						1.0	-	-	15.3		8.3		30.8		94.7		7.9										7.9		2.0			3		-	-	-		-				
					Middle	-	-	-	-	-	-	-	-	-	-	-	-										-		-		2.7	-	-	-	-	-	-	-	-	-	-	
						-	-	-	-		-		-		-		-												-			-		-	-	-	-	-	-	-		
					Bottom	3.3	-	-	15.5	15.5	8.3	8.3	31.3	31.3	94.8		7.8										7.8		3.4			5		-	-	-	-	-	-	-	-	-
						3.3	-	-	15.5		8.3		31.3		94.9		7.8												3.5			5		-	-	-	-	-	-	-	-	-

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 22 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity (µg/L)		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Rainy	Moderate	10:57	8.4	Surface	1.0	0.3	22	15.2	15.2	8.2	8.2	31.5	31.5	104.3	104.3	8.6		5.5		9		82		815606	804240	<0.2		0.7	
						1.0	0.3	18	15.2		8.2		31.5		104.2		8.6		5.6		8		82				<0.2		0.7	
					Middle	4.2	0.4	33	15.2	15.2	8.2	8.2	32.2	32.2	103.5	103.5	8.5	8.6	8.8	7.9	8	8	87	86			<0.2	<0.2	0.7	0.7
						4.2	0.5	32	15.2		8.2		32.2		103.5		8.5		8.9		8		87				<0.2		0.6	
					Bottom	7.4	0.3	20	15.3	15.3	8.2	8.2	32.4	32.3	104.2	104.2	8.6	8.6	9.5		6		90				<0.2		0.7	
						7.4	0.3	14	15.2		8.2		32.3		104.2		8.6		9.5		6		90				<0.2		0.6	
					Surface	1.0	0.3	359	15.5	15.5	8.2	8.2	30.9	30.9	101.9	101.9	8.4		3.7		3		82				<0.2		0.9	
						1.0	0.3	3	15.5	15.5	8.2	8.2	31.0	31.0	101.8	101.9	8.4	8.4	3.7		4		82				<0.2		0.9	
C2	Rainy	Moderate	12:14	10.7	Middle	5.4	0.3	349	15.9	15.9	8.2	8.2	31.6	31.6	101.5	101.6	8.3	8.4	4.2	3.9	5	5	87	86	825694	806938	<0.2	<0.2	0.8	0.8
						5.4	0.3	345	15.9		8.2		31.6		101.6		8.3		4.1		6		87				<0.2	<0.2	0.8	
					Bottom	9.7	0.4	1	16.0	16.0	8.2	8.2	31.7	31.7	102.1	102.2	8.3	8.3	3.8		6		90				<0.2		0.8	
						9.7	0.4	1	16.0		8.2		31.7		102.2		8.3		3.9		7		90				<0.2		0.8	
					Surface	1.0	0.4	260	15.6	15.6	8.1	8.1	31.6	31.6	92.6	92.6	7.6		2.4		4		83				<0.2		0.7	
						1.0	0.4	261	15.6		8.1		31.7		92.5		7.6	7.6	2.5		4		83				<0.2		0.6	
					Middle	5.7	0.4	273	15.7	15.7	8.1	8.1	31.8	31.8	92.4	92.4	7.6	7.6	7.4	5.9	4	4	86	87			<0.2	<0.2	0.6	0.6
						5.7	0.4	276	15.7		8.1		31.8		92.3		7.6		7.5		4		86				<0.2	<0.2	0.7	
C3	Rainy	Rough	09:42	11.3	Bottom	10.3	0.4	270	15.8	15.8	8.1	8.1	31.8	31.8	92.1	92.1	7.5	7.5	7.7		2		90		822093	817788	<0.2		0.6	
						10.3	0.3	276	15.8		8.1		31.8		92.1		7.5	7.5	7.8		3		91				<0.2		0.6	
					Surface	1.0	0.2	26	15.3	15.3	8.2	8.2	32.1	32.1	103.0	103.0	8.5		6.7		5		83				<0.2		0.6	
						1.0	0.3	24	15.3		8.2		32.1		103.0		8.5	8.5	6.3		5		83				<0.2		0.6	
					Middle	3.4	0.2	29	15.3	15.3	8.2	8.2	32.3	32.3	102.9	102.9	8.5	8.5	8.0	7.6	4	4	88	88			<0.2	<0.2	0.7	0.6
						3.4	0.3	31	15.3		8.2		32.3		102.9		8.5		8.0		4		88				<0.2	<0.2	0.6	
					Bottom	5.8	0.3	37	15.3	15.3	8.2	8.2	32.3	32.3	101.6	101.6	8.4	8.4	8.2		3		91				<0.2		0.7	
						5.8	0.3	39	15.3		8.2		32.3		101.6		8.4	8.4	8.2		3		92				<0.2		0.6	
IM2	Rainy	Moderate	11:25	7.0	Surface	1.0	0.2	28	15.1	15.1	8.2	8.2	31.6	31.6	104.3	104.3	8.6		4.9		4		83		819167	806216	<0.2		0.7	
						1.0	0.2	34	15.1		8.2		31.6		104.3		8.6	8.6	4.9		4		82				<0.2		0.6	
					Middle	3.5	0.3	18	15.2	15.2	8.2	8.2	31.8	31.8	103.4	103.4	8.6	8.6	5.6	5.9	6	5	87	87			<0.2	<0.2	0.6	0.6
						3.5	0.3	14	15.2		8.2		31.8		103.3		8.5		5.7		5		87				<0.2		0.7	
					Bottom	6.0	0.3	32	15.3	15.3	8.2	8.2	32.2	32.2	103.2	103.2	8.5	8.5	7.0		5		90				<0.2		0.6	
						6.0	0.2	29	15.3		8.2		32.2		103.2		8.5	8.5	7.1		6		90				<0.2		0.6	
					Surface	1.0	0.2	358	15.7	15.7	8.2	8.2	31.5	31.5	102.2	102.2	8.4		3.3		5		82				<0.2		0.6	
						1.0	0.3	359	15.7		8.2		31.5		102.2		8.4	8.4	3.3		5		82				<0.2		0.6	
IM7	Rainy	Moderate	11:47	7.6	Middle	3.8	0.2	336	15.7	15.7	8.2	8.2	31.7	31.7	101.7	101.7	8.3	8.4	3.4	3.4	3	4	86	86	821343	806811	<0.2	<0.2	0.7	0.7
						3.8	0.2	343	15.7		8.2		31.7		101.7		8.3		3.4		4		86				<0.2	<0.2	0.6	0.6
					Bottom	6.6	0.2	355	15.7	15.7	8.2	8.2	31.8	31.8	102.4	102.4	8.4	8.4	3.5		3		90				<0.2		0.8	
						6.6	0.1	357	15.7		8.2		31.8		102.4		8.4	8.4	3.5		4		90				<0.2		0.6	
					Surface	1.0	0.2	358	15.7	15.7	8.2	8.2	31.5	31.5	102.2	102.2	8.4		3.3		5		82				<0.2		0.6	
						1.0	0.3	359	15.7		8.2		31.5		102.2		8.4	8.4	3.3		5		82				<0.2		0.6	
					Middle	3.8	0.2	336	15.7	15.7	8.2	8.2	31.7	31.7	101.7	101.7	8.3	8.4	3.4	3.4	3	4	86	86			<0.2	<0.2	0.7	0.7
						3.8	0.2	343	15.7		8.2		31.7		101.7		8.3		3.4		4		86				<0.2	<0.2	0.6	0.6
					Bottom	6.6	0.2	355	15.7	15.7	8.2	8.2	31.8	31.8	102.4	102.4	8.4	8.4	3.5		3		90				<0.2		0.8	
						6.6	0.1	357	15.7		8.2		31.8		102.4		8.4	8.4	3.5		4		90				<0.2		0.6	

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 22 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)				
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	
IM10	Rainy	Rough	11:02	8.7	Surface	1.0	0.4	285	15.2	15.2	8.3	8.3	31.2	31.2	93.6	93.6	7.8	7.8	2.5	3.3	9	7	83	87	822242	809848	<0.2	<0.2	0.6	0.6			
						1.0	0.4	292	15.2	8.3	8.3	31.2	93.6	7.8	2.6	9	87		<0.2		0.6												
					Middle	4.4	0.4	283	15.2	8.3	8.3	31.2	93.6	7.8	3.1	6	83	<0.2	0.6														
						4.4	0.4	275	15.2	8.3	8.3	31.2	93.6	7.8	3.1	6	87	<0.2	0.6														
					Bottom	7.7	0.4	277	15.2	8.3	8.3	31.2	93.7	93.7	7.8	4.4	5	91	<0.2	0.6													
						7.7	0.4	283	15.2	8.3	8.3	31.2	93.7	7.8	4.4	6	91	<0.2	0.5														
IM11	Rainy	Rough	10:53	8.5	Surface	1.0	0.5	276	15.4	15.4	8.3	8.3	31.3	31.3	93.6	93.6	7.7	7.8	4.9	8.1	5	6	83	87	821504	810555	<0.2	<0.2	0.7	0.6			
						1.0	0.5	272	15.4	8.3	8.3	31.3	93.6	7.7	4.9	4	83		<0.2		0.5												
					Middle	4.3	0.5	281	15.3	15.3	8.3	8.3	31.3	93.8	93.8	7.8	8.8	5	87	<0.2	0.6												
						4.3	0.5	284	15.3	8.3	8.3	31.3	93.8	7.8	8.8	6	87	<0.2	0.6														
					Bottom	7.5	0.5	274	15.3	15.3	8.3	8.3	31.2	94.4	94.5	7.8	10.8	6	90	<0.2	0.5												
						7.5	0.5	278	15.3	8.3	8.3	31.3	94.5	7.8	10.8	7	90	<0.2	0.6														
IM12	Rainy	Rough	10:47	9.4	Surface	1.0	0.5	297	15.4	15.4	8.3	8.3	31.3	31.3	93.4	93.4	7.7	7.7	2.8	4.1	5	7	79	83	821168	811506	<0.2	<0.2	0.6	0.6			
						1.0	0.5	289	15.4	8.3	8.3	31.3	93.4	7.7	2.8	6	79		<0.2		0.5												
					Middle	4.7	0.5	280	15.4	15.4	8.3	8.3	31.4	93.4	93.5	7.7	4.1	8	83	<0.2	0.6												
						4.7	0.5	274	15.4	8.3	8.3	31.4	93.5	7.7	4.2	7	83	<0.2	0.6														
					Bottom	8.4	0.5	275	15.4	15.4	8.3	8.3	31.3	94.5	94.6	7.8	5.3	9	90	<0.2	0.6												
						8.4	0.5	278	15.4	8.3	8.3	31.3	94.7	7.8	5.3	9	90	<0.2	0.6														
SR1A	Rainy	Moderate	10:17	4.7	Surface	1.0	0.1	197	15.1	15.1	8.2	8.2	30.7	30.7	92.0	92.0	7.7	7.7	3.9	2.9	7	7	-	-	819972	812664	-	-	-	-			
						1.0	0.0	202	15.1	8.2	8.2	30.7	92.0	7.7	4.0	8	-		-		-												
					Middle	2.4	0.1	211	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-
						2.4	0.0	215	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	
					Bottom	3.7	0.0	175	15.1	15.1	8.2	8.2	30.7	93.0	93.1	7.8	1.9	5	-	-	-	-	-	-			-		-		-	-	-
						3.7	0.1	173	15.1	8.3	8.2	30.7	93.2	93.1	7.8	1.9	6	-	-	-	-	-	-	-			-		-		-	-	
SR2	Rainy	Moderate	10:00	5.3	Surface	1.0	0.1	255	15.5	15.5	8.2	8.2	31.5	31.5	94.7	94.8	7.8	7.8	2.1	2.3	7	6	82	82	821452	814151	<0.2	<0.2	0.6	0.6			
						1.0	0.1	255	15.5	8.2	8.2	31.5	94.9	7.8	2.1	8	82		<0.2		0.7												
					Middle	-	0.1	256	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-
						-	0.1	251	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	
					Bottom	4.3	0.1	270	15.4	15.4	8.2	8.2	31.5	96.1	96.2	7.9	2.4	5	87	<0.2	0.5												
						4.3	0.1	274	15.4	8.2	8.2	31.5	96.3	7.9	2.5	4	87	<0.2	0.6														
SR3	Rainy	Moderate	11:55	8.6	Surface	1.0	0.3	327	15.8	15.8	8.2	8.2	31.6	31.6	102.7	102.7	8.4	8.4	3.5	3.5	3	3	-	-	822136	807561	-	-	-	-			
						1.0	0.3	331	15.8	8.2	8.2	31.6	102.7	8.4	3.5	2	-		-		-												
					Middle	4.3	0.3	326	15.7	15.7	8.2	8.2	31.8	102.5	102.5	8.4	3.5	3	-	-	-	-	-	-			-		-		-	-	
						4.3	0.3	321	15.7	8.2	8.2	31.8	102.5	8.4	3.5	4	-	-	-	-	-	-	-	-			-		-		-		
					Bottom	7.6	0.3	337	15.7	15.7	8.2	8.2	31.8	102.6	102.6	8.4	3.7	4	-	-	-	-	-	-			-		-		-	-	
						7.6	0.3	331	15.7	8.2	8.2	31.8	102.6	8.4	3.7	4	-	-	-	-	-	-	-	-			-		-		-		
SR4A	Rainy	Calm	10:34	8.8	Surface	1.0	0.0	217	15.3	15.3	8.2	8.2	30.9	30.9	101.3	101.3	8.4	8.4	4.2	4.7	5	6	-	-	817172	807786	-	-	-	-			
						1.0	0.0	212	15.3	8.2	8.2	30.9	101.3	8.4	4.2	4	-		-		-												
					Middle	4.4	0.0	198	15.3	15.3	8.2	8.2	31.2	101.6	101.6	8.4	4.4	6	-	-	-	-	-	-			-		-		-	-	
						4.4	0.0	192	15.3	8.2	8.2	31.2	101.6	8.4	4.4	6	-	-	-	-	-	-	-	-			-		-		-		
					Bottom	7.8	0.0	232	15.3	15.3	8.2	8.2	32.1	103.4	103.8	8.5	5.4	6	-	-	-	-	-	-			-		-		-	-	
						7.8	0.0	238	15.3	8.2	8.2	32.0	104.2	8.6	5.4	7	-	-	-	-	-	-	-	-			-		-		-		
SR8	Rainy	Moderate	10:41	5.5	Surface	1.0	-	-	15.3	15.3	8.3	8.3	31.2	31.2	93.9	93.9	7.8	7.8	2.6	2.8	6	7	-	-	820391	811614	-	-	-	-			
						1.0	-	-	15.3	8.3	8.3	31.2	93.9	7.8	2.7	6	-		-		-												
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	-
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-		-		-	-	
					Bottom	4.5	-	-	15.3	15.3	8.3	8.3	31.2	94.5	94.6	7.8	2.9	7	-	-	-	-	-	-			-		-		-	-	-
						4.5	-	-	15.3	8.3	8.3	31.2	94.6	7.8	2.9	7	-	-	-	-	-	-	-	-			-		-		-	-	

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 24 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)			
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA
C1	Cloudy	Rough	04:50	8.3	Surface	1.0	0.0	53	15.3	15.3	8.3	8.3	31.6	31.6	102.4	102.6	8.4	8.5	6.7	8.7	3		82		815615	804232	<0.2	0.4	0.4			
						1.0	0.1	52	15.3		8.3	8.3	31.6	31.6	102.7	102.6	8.5	8.5	6.5	2	82		<0.2	0.4								
					Middle	4.2	0.0	51	15.1	15.1	8.2	8.2	32.2	32.2	103.8	104.0	8.6	8.6	9.0	2	87	86	<0.2	0.4								
						4.2	0.0	43	15.1		8.2	8.2	32.2	32.2	104.1	104.0	8.6	8.6	9.2	4	87		<0.2	0.4								
					Bottom	7.3	0.0	44	15.1	15.1	8.2	8.2	32.5	32.3	102.4	102.4	8.5	8.5	10.5	3	90		<0.2	0.4								
						7.3	0.0	38	15.1		8.2	8.2	32.1	32.3	102.4	102.4	8.4	8.5	10.4	4	90		<0.2	0.3								
C2	Cloudy	Rough	06:04	11.0	Surface	1.0	0.1	182	15.5	15.5	8.2	8.2	30.8	30.9	103.3	103.4	8.4	8.4	2.5	3.2	2		83		825702	806931	<0.2	0.4	0.4			
						1.0	0.1	186	15.5		8.2	8.2	31.0	31.0	103.5	103.4	8.6	8.4	2.8	3	82		<0.2	0.4								
					Middle	5.5	0.1	174	16.0	16.0	8.1	8.1	31.6	31.6	101.9	101.7	8.4	8.3	3.4	2	87	87	<0.2	0.4								
						5.5	0.1	175	16.0		8.1	8.1	31.5	31.5	101.5	101.5	8.3	8.3	3.8	3	87		<0.2	0.4								
					Bottom	10.0	0.2	191	16.0	16.0	8.3	8.3	31.8	31.7	101.7	101.5	8.3	8.3	3.3	2	90		<0.2	0.4								
						10.0	0.2	196	16.0		8.3	8.3	31.5	31.5	101.3	101.3	8.2	8.3	3.4	3	90		<0.2	0.4								
C3	Cloudy	Rough	04:27	11.3	Surface	1.0	0.1	283	15.6	15.6	8.3	8.3	31.6	31.7	92.4	92.3	7.6	7.5	3.7	6.3	3		82		822089	817793	<0.2	0.5	0.4			
						1.0	0.1	277	15.6		8.3	8.3	31.8	31.7	92.2	92.3	7.6	7.5	3.3	3	82		<0.2	0.4								
					Middle	5.7	0.1	251	15.6	15.6	8.2	8.2	31.6	31.7	90.3	90.4	7.4	7.4	8.6	3	86	86	<0.2	0.3								
						5.7	0.1	244	15.6		8.2	8.2	31.8	31.7	90.4	90.4	7.4	7.4	8.4	3	86		<0.2	0.3								
					Bottom	10.3	0.0	268	15.7	15.7	8.1	8.1	31.7	31.7	92.8	93.0	7.6	7.6	6.6	4	90		<0.2	0.3								
						10.3	0.0	272	15.7		8.1	8.1	31.7	31.7	93.1	93.0	7.6	7.6	6.9	3	91		<0.2	0.4								
IM1	Cloudy	Rough	05:09	6.4	Surface	1.0	0.1	181	15.3	15.3	8.2	8.2	32.2	32.2	101.0	100.9	8.3	8.4	6.6	7.6	5		83		818333	806446	<0.2	0.4	0.4			
						1.0	0.1	186	15.3		8.2	8.2	32.2	32.2	100.8	100.8	8.3	8.4	6.5	4	83		<0.2	0.3								
					Middle	3.2	0.0	165	15.3	15.3	8.2	8.2	32.3	32.4	103.0	103.1	8.5	8.5	8.7	3	88	88	<0.2	0.4								
						3.2	-	168	15.3		8.2	8.2	32.5	32.4	103.1	103.1	8.5	8.5	8.9	4	88		<0.2	0.4								
					Bottom	5.4	0.0	203	15.2	15.2	8.1	8.1	32.4	32.3	103.2	103.0	8.5	8.5	7.5	3	92		<0.2	0.5								
						5.4	0.0	198	15.2		8.1	8.1	32.2	32.3	102.7	103.0	8.5	8.5	7.3	4	92		<0.2	0.3								
IM2	Cloudy	Rough	05:16	7.3	Surface	1.0	0.0	152	15.0	15.0	8.3	8.3	31.7	31.7	105.3	105.2	8.6	8.5	4.1	5.6	3		83		819161	806226	<0.2	0.4	0.4			
						1.0	0.0	157	15.0		8.3	8.3	31.6	31.7	105.1	105.1	8.7	8.5	4.4	2	83		<0.2	0.3								
					Middle	3.7	0.0	164	15.3	15.3	8.1	8.1	31.6	31.7	100.9	100.9	8.3	8.3	4.9	3	87	87	<0.2	0.4								
						3.7	0.1	163	15.3		8.1	8.1	31.7	31.7	100.8	100.8	8.3	8.3	4.9	2	87		<0.2	0.4								
					Bottom	6.3	0.1	161	15.4	15.4	8.1	8.1	32.3	32.3	103.2	103.4	8.5	8.5	7.4	3	90		<0.2	0.4								
						6.3	0.1	165	15.4		8.1	8.1	32.2	32.3	103.6	103.4	8.5	8.5	7.7	4	90		<0.2	0.4								
IM7	Cloudy	Rough	05:37	7.4	Surface	1.0	0.1	148	15.7	15.7	8.1	8.1	31.6	31.7	101.1	101.3	8.3	8.4	3.5	3.1	3		82		821349	806806	<0.2	0.3	0.4			
						1.0	0.1	150	15.7		8.1	8.1	31.7	31.7	101.4	101.4	8.3	8.4	3.2	2	82		<0.2	0.4								
					Middle	3.7	0.1	144	15.7	15.7	8.1	8.1	31.8	31.9	102.5	102.6	8.4	8.4	2.5	3	86	86	<0.2	0.3								
						3.7	0.1	140	15.7		8.1	8.1	31.9	31.9	102.7	102.7	8.4	8.4	2.5	3	86		<0.2	0.4								
					Bottom	6.4	0.1	171	15.7	15.7	8.4	8.4	31.9	31.9	103.1	103.2	8.4	8.5	3.3	4	90		<0.2	0.3								
						6.4	0.1	175	15.7		8.4	8.4	31.8	31.9	103.3	103.2	8.5	8.5	3.3	3	90		<0.2	0.4								

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 24 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)								
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	Value	DA	
IM10	Cloudy	Rough	06:25	8.7	Surface	1.0	0.1	107	15.2	15.2	8.2	8.2	31.3	31.3	91.3	91.4	7.3	7.5	2.8	3.8	3	5	82	87	822248	809856	<0.2	0.3	0.4								
						1.0	0.1	102	15.2		8.2	8.2	31.2	31.2	91.5	91.0	7.6		2.9		3		87				<0.2	0.4									
					Middle	4.4	0.2	120	15.2	8.3	8.3	31.2	31.2	91.0	91.1	7.5	3.0	5	82	<0.2	0.4																
						4.4	0.2	126	15.2	8.3	8.3	31.1	31.2	91.2	91.1	7.6	3.4	4	88	<0.2	0.4																
					Bottom	7.7	0.2	134	15.3	8.4	8.4	31.3	31.3	94.3	94.3	7.8	5.5	6	90	<0.2	0.3																
						7.7	0.2	135	15.3	8.4	8.4	31.3	31.3	94.2	94.3	7.8	5.2	6	91	<0.2	0.4																
						1.0	0.1	92	15.3	8.4	8.4	31.1	31.3	93.7	93.9	7.8	4.2	3	83	<0.2	0.4																
						1.0	0.1	92	15.3	8.4	8.4	31.4	31.3	94.1	94.0	7.8	4.5	2	83	<0.2	0.2																
IM11	Cloudy	Rough	05:55	8.5	Surface	4.3	0.1	105	15.4	15.4	8.1	8.1	31.3	31.3	94.6	94.5	7.8	7.8	9.7	8.5	3	3	87	87	821515	810559	<0.2	0.4	0.3								
						4.3	0.1	105	15.4		8.1	8.1	31.2	31.3	94.4	94.5	7.8		9.6		3		87				<0.2	0.3									
					Bottom	7.5	0.1	115	15.3	8.3	8.3	31.1	31.2	94.1	94.0	7.8	11.6	2	90	<0.2	0.3																
						7.5	0.1	115	15.3	8.3	8.3	31.2	31.2	93.9	94.0	7.8	11.1	2	90	<0.2	0.3																
					1.0	0.1	111	15.3	8.4	8.4	31.2	31.3	95.1	95.2	7.9	2.0	3	79	<0.2	0.4																	
					1.0	0.0	107	15.3	8.4	8.4	31.3	31.3	95.2	95.2	7.9	2.1	2	79	<0.2	0.3																	
					IM12	Cloudy	Rough	05:37	9.4	Surface	4.7	0.1	90	15.3	15.3	8.2	8.2	31.2	31.4	92.2	92.2	7.6	7.8	4.7			4.2	3		3	82	82	821161	811518	<0.2	0.4	0.4
											4.7	0.1	89	15.3		8.2	8.2	31.5	31.4	92.1	92.2	7.6		5.0				4			82				<0.2	0.3	
Bottom	8.4	0.1	76	15.5						8.1	8.1	31.3	31.3	95.5	95.4	7.9	5.7	4	90	<0.2	0.4																
	8.4	0.0	77	15.5						8.1	8.1	31.3	31.3	95.2	95.4	7.8	5.4	4	90	<0.2	0.3																
SR1A	Cloudy	Rough	05:13	4.7	Surface	1.0	0.0	6	15.0	15.0	8.1	8.1	30.7	30.7	93.5	93.5	7.7	7.8	2.8	2.5	2	2	-	-	819979	812651	-	-	-								
						1.0	0.0	7	15.0		8.1	8.1	30.6	30.7	93.5	93.5	7.8		3.1		2		-				-										
					Middle	2.4	0.0	357	-	-	-	-	-	-	-	-	-	-	-	-	-	2	-	-			-	-		-	-	-					
						2.4	0.0	3	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-		-	-	-					
					Bottom	3.7	0.0	-	15.0	8.2	8.2	30.7	30.8	93.5	93.3	7.8	2.0	2	-	-	-	-	-	-			-	-		-	-	-	-				
						3.7	0.0	359	15.0	8.2	8.2	30.9	30.8	93.0	93.3	7.8	2.0	2	-	-	-	-	-	-			-	-		-	-	-	-				
					SR2	Cloudy	Rough	04:49	5.3	Surface	1.0	0.0	316	15.6	15.6	8.2	8.2	31.5	31.5	95.6	95.7	8.0	8.0	0.9			2.1	2		3	82	82	821454	814157	<0.2	0.3	0.4
											1.0	0.1	313	15.6		8.2	8.2	31.4	31.5	95.8	95.7	7.9		1.0				2			82				<0.2	0.4	
Middle	-	-	342	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-							
	-	0.1	334	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-							
Bottom	4.3	0.0	321	15.3						8.3	8.3	31.6	31.6	97.3	97.4	8.0	3.4	3	87	<0.2	0.4																
	4.3	0.0	314	15.3						8.3	8.3	31.5	31.6	97.4	97.4	8.0	3.2	3	87	<0.2	0.3																
SR3	Cloudy	Rough	05:45	8.7						Surface	1.0	0.1	151	15.9	15.9	8.3	8.3	31.7	31.7	100.1	100.2	8.1	8.2	3.8	3.9	3	3	-	-	822128	807564	-			-	-	
											1.0	0.1	144	15.9		8.3	8.3	31.7	31.7	100.2	100.2	8.2		3.9		3		-				-					
					Middle	4.4	0.1	176	15.8	8.2	8.2	31.8	31.8	99.8	100.0	8.2	4.4	2	-	-	-	-	-	-	-	-	-	-	-								
						4.4	0.1	178	15.8	8.2	8.2	31.7	31.8	100.2	100.0	8.2	4.0	3	-	-	-	-	-	-	-	-	-	-	-								
					Bottom	7.7	0.1	179	15.8	8.2	8.2	31.7	31.9	105.4	105.2	8.6	3.6	2	-	-	-	-	-	-	-	-	-	-	-			-					
						7.7	0.0	177	15.8	8.2	8.2	32.0	31.9	105.0	105.2	8.6	3.4	2	-	-	-	-	-	-	-	-	-	-	-			-					
					SR4A	Cloudy	Rough	04:31	8.6	Surface	1.0	0.0	303	15.2	15.2	8.3	8.3	30.8	30.9	101.5	101.5	8.4	8.4	5.1	4.4	2	3	-	-			817179	807783	-	-		-
											1.0	0.0	296	15.2		8.3	8.3	31.0	30.9	101.5	101.5	8.4		4.6		2		-						-			
Middle	4.3	0.0	297	15.4						8.2	8.2	31.1	31.1	100.2	100.5	8.3	4.1	2	-	-	-	-	-	-	-	-	-	-	-								
	4.3	0.1	303	15.4						8.2	8.2	31.1	31.1	100.7	100.7	8.4	3.7	3	-	-	-	-	-	-	-	-	-	-	-								
Bottom	7.6	0.0	310	15.2						8.1	8.1	32.1	32.1	104.0	104.0	8.6	4.6	3	-	-	-	-	-	-	-	-	-	-	-								
	7.6	0.0	312	15.2						8.1	8.1	32.0	32.1	104.0	104.0	8.6	4.4	3	-	-	-	-	-	-	-	-	-	-	-								
SR8	Cloudy	Rough	05:26	5.5						Surface	1.0	-	-	15.3	15.3	8.1	8.1	31.2	31.2	91.9	92.0	7.6	7.6	2.7	2.7	3	4	-	-	820384	811607			-	-	-	
											1.0	-	-	15.3		8.1	8.1	31.1	31.2	92.0	92.0	7.6		2.7		3		-						-			
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-					
						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-								
					Bottom	4.5	-	-	15.4	8.2	8.2	31.3	31.2	96.7	96.8	8.0	2.8	-	-	-	-	-	-	-	-	-	-	-	-			-					
						4.5	-	-	15.4	8.2	8.2	31.1	31.2	96.8	96.8	8.0	2.6	6	-	-	-	-	-	-	-	-	-	-	-								

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 24 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)									
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA	Value	DA		
C1	Cloudy	Rough	12:05	8.7	Surface	1.0	0.2	44	15.2	15.2	8.1	8.1	31.2	31.3	107.0	107.0	8.8	8.7	5.4	8.6	3	3	82	87	815644	804240	<0.2	<0.2	0.4	0.4								
						1.0	0.2	47	15.2		8.1		31.3		107.0		8.9		5.5		3		82				<0.2		0.3									
					Middle	4.4	0.3	33	15.6	15.6	8.2	8.2	32.3	32.3	103.6	103.5	8.6	8.5	9.4	8.5	3	3	88	90			<0.2	<0.2	0.4		0.4							
						4.4	0.2	27	15.6	8.2	32.3		103.3		8.4		9.4		4		88		<0.2				0.5											
					Bottom	7.7	0.3	32	15.4	15.4	8.3	8.3	32.4	32.5	103.8	103.9	8.5	8.5	10.9	8.5	4	3	90	91			<0.2	<0.2	0.4		0.5							
						7.7	0.3	36	15.4	8.3	32.5		103.9		8.5		10.9		3		91		<0.2				0.5											
					C2	Cloudy	Rough	10:11	10.7	Surface	1.0	0.0	204	15.6	15.6	8.2	8.2	30.9	31.0	101.4	101.5	8.3	8.4	4.0			3.3	3	3		82	86	825693	806944	<0.2	<0.2	0.4	0.4
											1.0	0.0	204	15.6		8.2		31.0		101.5		8.4		3.7				3			82				<0.2		0.4	
Middle	5.4	0.1	174	15.8						15.8	8.3	8.3	31.6	31.6	102.8	102.8	8.5	8.4	3.6	3.3	3	3	86	91	<0.2	<0.2	0.3	0.4										
	5.4	0.1	174	15.8						8.3	31.6		102.7		8.4		3.5		3		86		<0.2		0.3													
Bottom	9.7	0.1	177	15.8						15.8	8.3	8.3	31.7	31.7	106.5	106.5	8.7	8.7	2.4	3.3	3	3	91	91	<0.2	<0.2	0.4	0.4										
	9.7	0.1	181	15.8						8.3	31.7		106.4		8.7		2.5		3		91		<0.2		0.4													
C3	Cloudy	Rough	12:27	10.5						Surface	1.0	0.4	251	15.5	15.6	8.3	8.3	31.6	31.7	91.1	92.4	7.3	7.6	1.4	1.8	3	4	82	86	822107	817830	<0.2			<0.2	0.3	0.4	
											1.0	0.4	256	15.7		8.2		31.7		93.6		7.7		1.5		3		82				<0.2				0.3		
					Middle	5.3	0.4	279	15.7	15.8	8.2	8.3	31.7	31.7	93.8	92.6	7.7	7.5	1.4	7.5	3	4	87	90	<0.2	<0.2	0.4	0.3										
						5.3	0.4	283	15.8	8.4	31.6		91.3		7.5		1.4		4		87		<0.2		0.3													
					Bottom	9.5	0.4	268	15.8	15.8	8.4	8.4	31.7	31.8	91.1	91.5	7.4	7.5	2.3	7.5	5	6	90	90	<0.2	<0.2	0.5	0.5										
						9.5	0.4	274	15.7	8.4	31.8		91.8		7.5		2.6		6		90		<0.2		0.5													
					IM1	Cloudy	Rough	11:45	6.4	Surface	1.0	0.2	4	15.1	15.1	8.3	8.3	31.4	31.5	105.3	105.4	8.6	8.6	3.9	4.9	4	4	82	87			818349	806446	<0.2	<0.2	0.5		0.5
											1.0	0.2	6	15.1		8.3		31.5		105.4		8.7		4.3		5		82						<0.2		0.4		
Middle	3.2	0.2	-	15.2						15.2	8.1	8.1	32.2	32.2	102.1	102.0	8.5	8.5	4.2	4.8	3	4	87	91	<0.2	<0.2	0.6	0.4										
	3.2	0.2	5	15.2						8.1	32.2		101.9		8.4		4.7		4		87		<0.2		0.4													
Bottom	5.4	0.2	35	15.3						15.3	8.4	8.4	32.4	32.3	106.2	106.3	8.8	8.8	6.0	8.8	3	3	91	91	<0.2	<0.2	0.4	0.5										
	5.4	0.2	29	15.3						8.4	32.1		106.4		8.7		6.0		3		91		<0.2		0.5													
IM2	Cloudy	Rough	11:27	6.3						Surface	1.0	0.1	350	15.3	15.3	8.2	8.2	31.6	31.7	103.6	103.6	8.5	8.5	4.9	4.8	6	4	83	87	819179	806251			<0.2	<0.2	0.4	0.4	
											1.0	0.1	349	15.3		8.2		31.8		103.6		8.6		4.5		5		84						<0.2		0.4		
					Middle	3.2	0.1	336	15.1	15.1	8.1	8.1	32.2	32.2	101.9	102.0	8.4	8.4	5.0	8.7	4	4	87	92	<0.2	<0.2	0.4	0.4										
						3.2	0.1	339	15.1	8.1	32.1		102.1		8.4		4.8		4		87		<0.2		0.4													
					Bottom	5.3	0.1	328	15.1	15.1	8.4	8.4	32.3	32.3	105.7	105.7	8.7	8.7	4.9	8.7	4	3	92	91	<0.2	<0.2	0.4	0.4										
						5.3	0.1	321	15.1	8.4	32.2		105.6		8.7		4.4		3		91		<0.2		0.4													
					IM7	Cloudy	Rough	11:16	7.3	Surface	1.0	0.1	302	15.2	15.2	8.1	8.1	32.1	32.1	103.0	102.9	8.5	8.6	4.3	4.2	5	6	83	88			821359	806861	<0.2	<0.2	0.5		0.4
											1.0	0.1	299	15.2		8.1		32.0		102.8		8.5		4.6		4		82						<0.2		0.5		
Middle	3.7	0.1	309	15.4						15.4	8.3	8.3	32.1	32.1	104.4	104.5	8.6	8.6	3.8	8.6	6	6	88	92	<0.2	<0.2	0.3	0.4										
	3.7	0.1	302	15.4						8.3	32.1		104.6		8.6		3.7		6		88		<0.2		0.4													
Bottom	6.3	0.1	310	15.3						15.3	8.2	8.2	31.9	32.0	104.8	104.8	8.6	8.6	4.3	8.6	6	7	92	92	<0.2	<0.2	0.4	0.4										
	6.3	0.2	311	15.3						8.2	32.0		104.8		8.6		4.5		7		92		<0.2		0.4													

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 24 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)					
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA
IM10	Cloudy	Rough	10:11	8.2	Surface	1.0	0.1	263	15.4	15.4	8.4	8.3	31.2	31.3	95.4	94.6	7.9	7.8	4.4	4.6	5	7	82	86	822241	809826	<0.2	0.3	0.4					
						1.0	0.1	260	15.4		8.1		31.3		93.7		7.7		4.2		6		82				<0.2			0.4				
					Middle	4.1	0.1	245	15.4	15.5	8.1	8.2	31.5	31.5	93.8	93.7	7.7	7.8	3.4	7	86	<0.2	0.4											
						4.1	0.1	249	15.5	8.2	31.4		93.5		7.7		3.5		7		86	<0.2	0.3											
					Bottom	7.2	0.1	263	15.5	15.5	8.2	8.2	31.2	31.3	93.2	92.2	7.7	7.8	5.9	7	90	<0.2	0.4											
						7.2	0.1	264	15.4	15.5	8.2		31.4		91.2		7.8		6.0		7	90	<0.2	0.3										
						1.0	0.2	257	15.4	15.5	8.4		8.3		31.5		31.5		95.7		94.3	7.9	7.8	1.2			6	79		<0.2	0.3			
						1.0	0.2	257	15.6	15.5	8.1				31.4				92.8			7.7		1.3				5		78	<0.2	0.4		
Middle	4.1	0.2	257	15.6	15.6	8.1	8.1	31.6	31.5	92.8	94.1	7.6	7.8	2.2	3	87	<0.2	0.4																
	4.1	0.3	253	15.6	15.6	8.1		31.4		95.3		7.8		2.0		4	87	<0.2	0.3															
	Bottom	7.1	0.2	276	15.6	15.5	8.1	8.3	31.4	31.5	95.4	95.4	7.8	7.8	3.1	4	91	<0.2	0.3															
		7.1	0.1	274	15.4	15.5	8.4		31.5		95.3		7.8		3.3		3	91	<0.2	0.4														
IM11	Cloudy	Rough	10:43	8.1	Surface	1.0	0.2	257	15.4	15.5	8.4	8.3	31.5	31.5	95.7	94.3	7.9	7.8	1.2	6	79	<0.2	0.3											
						1.0	0.2	257	15.6		15.5		8.1		31.4		92.8		7.7		1.3	5	78	<0.2	0.4									
					Middle	4.1	0.2	257	15.6	15.6	8.1	8.1	31.6	31.5	92.8	94.1	7.6	7.8	2.2	3	87	<0.2	0.4											
						4.1	0.3	253	15.6	15.6	8.1		31.4		95.3		7.8		2.0		4	87	<0.2	0.3										
					Bottom	7.1	0.2	276	15.6	15.5	8.1	8.3	31.4	31.5	95.4	95.4	7.8	7.8	3.1	4	91	<0.2	0.3											
						7.1	0.1	274	15.4	15.5	8.4		31.5		95.3		7.8		3.3		3	91	<0.2	0.4										
					Surface	1.0	0.3	272	15.7	15.7	8.3	8.3	31.5	31.5	92.7	93.5	7.6	7.7	2.0	2	79	<0.2	0.4											
						1.0	0.3	276	15.7	15.7	8.2		31.4		94.3		7.7		2.2		3	79	<0.2	0.4										
Middle	4.7	0.3	264	15.7		15.7	8.2	8.2	31.4	31.4	94.6	94.9	7.8	7.7	2.3	2	83	<0.2	0.4															
	4.7	0.2	266	15.7		15.7	8.2		31.4		95.2		7.8		2.2		3	83	<0.2	0.3														
Bottom	8.4	0.3	280	15.7	15.6	8.2	8.3	31.6	31.5	95.4	95.4	7.8	7.8	1.0	3	87	<0.2	0.3																
	8.4	0.3	277	15.4	15.6	8.4		31.4		95.4		7.8		1.1		2	87	<0.2	0.3															
IM12	Cloudy	Rough	11:16	9.4	Surface	1.0	0.3	272	15.7	15.7	8.3	8.3	31.5	31.5	92.7	93.5	7.6	7.7	2.0	1.8	2	3	79	<0.2	0.4									
						1.0	0.3	276	15.7		15.7		8.2		31.4		94.3		7.7		2.2		3	79	<0.2	0.4								
					Middle	4.7	0.3	264	15.7	15.7	8.2	8.2	31.4	31.4	94.6	94.9	7.8	7.7	2.3	2	83	<0.2	0.4											
						4.7	0.2	266	15.7	15.7	8.2		31.4		95.2		7.8		2.2		3	83	<0.2	0.3										
					Bottom	8.4	0.3	280	15.7	15.6	8.2	8.3	31.6	31.5	95.4	95.4	7.8	7.8	1.0	3	87	<0.2	0.3											
						8.4	0.3	277	15.4	15.6	8.4		31.4		95.4		7.8		1.1		2	87	<0.2	0.3										
					Surface	1.0	0.0	213	15.2	15.2	8.4	8.4	30.6	30.6	94.5	93.0	7.8	7.7	3.2	2.2	7	-	5	-	-	-	-	-						
						1.0	0.0	219	15.2	15.2	8.3		30.5		91.4		7.6		2.8		6	-		-	-	-								
Middle	2.4	0.0	234	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-												
	2.4	0.0	239	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-												
Bottom	3.8	0.0	216	15.2	15.3	8.3	8.3	30.7	30.6	91.1	93.6	7.6	7.8	1.4	7.8	4	-	-	-	-	-	-	-											
	3.8	0.1	216	15.4	15.3	8.3		30.5		96.1		8.0		1.5		4	-	-	-	-														
SR1A	Cloudy	Rough	11:45	4.8	Surface	1.0	0.0	213	15.2	15.2	8.4	8.4	30.6	30.6	94.5	93.0	7.8	7.7	3.2	2.2	7	-	5	-	819979	812677	-	-	-					
						1.0	0.0	219	15.2		15.2		8.3		30.5		91.4		7.6		2.8	6		-			-	-	-					
					Middle	2.4	0.0	234	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-	-					
						2.4	0.0	239	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-	-	-					
					Bottom	3.8	0.0	216	15.2	15.3	8.3	8.3	30.7	30.6	91.1	93.6	7.6	7.8	1.4	7.8	4	-	-	-			-	-	-	-				
						3.8	0.1	216	15.4	15.3	8.3		30.5		96.1		8.0		1.5		4	-	-	-			-							
					Surface	1.0	0.1	272	15.7	15.7	8.4	8.3	31.6	31.6	91.5	94.5	7.5	7.8	2.2	2.7	4	83	<0.2	0.4										
						1.0	0.1	266	15.7	15.7	8.2		31.6		97.4		8.0		2.3		3	83	<0.2	0.3										
Middle	-	0.1	277	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-											
	-	0.1	278	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-											
Bottom	4.1	0.1	249	15.7	15.5	8.2	8.3	31.8	31.7	97.8	96.4	8.0	7.9	3.1	7.9	3	87	<0.2	0.3															
	4.1	0.1	246	15.2	15.5	8.4		31.6		94.9		7.8		3.3		2	87	<0.2	0.4															
SR2	Cloudy	Rough	12:05	5.1	Surface	1.0	0.1	272	15.7	15.7	8.4	8.3	31.6	31.6	91.5	94.5	7.5	7.8	2.2	2.7	4	83	<0.2	0.4										
						1.0	0.1	266	15.7		15.7		8.2		31.6		97.4		8.0		2.3	3	83	<0.2	0.3									
					Middle	-	0.1	277	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-							
						-	0.1	278	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-							
					Bottom	4.1	0.1	249	15.7	15.5	8.2	8.3	31.8	31.7	97.8	96.4	8.0	7.9	3.1	7.9	3	87	<0.2	0.3										
						4.1	0.1	246	15.2	15.5	8.4		31.6		94.9		7.8		3.3		2	87	<0.2	0.4										
					Surface	1.0	0.0	258	15.3	15.3	8.1	8.1	31.6	31.7	100.7	100.7	8.3	8.4	5.8	5.9	3	-	4	-	-	-	-	-						
						1.0	0.0	260	15.3		15.3		8.1		31.8		100.7		8.3		5.8	2		-	-	-	-							
Middle	4.3	0.1	271	15.2		15.2	8.3	8.3	31.8	31.9	101.4	101.5	8.4	8.4	5.4	5.9	3	-	-	-	-	-	-											
	4.3	0.0	275	15.2		15.2	8.3		31.9		101.5		8.4		5.8		4	-	-	-	-													
Bottom	7.6	0.1	248	15.4	15.4	8.4	8.4	31.7	31.9	101.6	101.9	8.4	8.4	6.5	5.9	4	-	-	-	-	-	-	-											
	7.6	0.2	245	15.4	15.4	8.4		32.0		102.1		8.4		6.2		5	-	-	-	-														
SR3	Cloudy	Rough	10:43	8.6	Surface	1.0	0.1	222	15.1	15.1	8.3	8.3	31.9	31.9	104.8	105.0	8.3	8.6	5.0	4.7	7	-	5	-	817203	807791	-	-	-					
						1.0	0.1	223	15.1		15.1		8.3		31.9		105.1		8.7		5.1	6		-			-	-	-					
					Middle	4.3	0.0	217	15.0	15.0	8.2	8.2	31.9	32.0	103.9	104.1	8.6	8.8	3.3	5.9	5	-	-	-			-	-	-	-				
						4.3	-	222	15.0	15.0	8.2		32.0		104.2		8.6		3.6		5	-	-	-			-							
					Bottom	7.5	0.0	225	15.2	15.2	8.3	8.3	32.3	32.2	106.3	106.3	8.8	8.8	5.5	5.9	4	-	-	-			-	-	-	-				
						7.5	0.0	226	15.2	15.2	8.3		32.1		106.2		8.7		5.4		4	-	-	-			-							
					Surface	1.0	-	-	15.4	15.4	8.3	8.2	30.7	30.8	96.4	94.1	8.0	7.8	2.4	2.3	4	-	5	-			-	-	-	-	-			
						1.0	-	-	15.4		15.4		8.1		30.8		91.8		7.6		2.5	5		-			-	-	-					
Middle	-	-	-	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-										
	-	-	-	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-										
Bottom	3.3	-	-	15.4	15.6	8.1	8.2	31.2	31.2	92.3	92.8	7.6	7.7	2.1	2.3	5	-	-	-	-	-	-	-	-										
	3.3	-	-	15.7		15.7		8.3		31.2		93.2		7.7		2.2	5	-	-	-	-													
SR4A	Cloudy	Rough	12:26	8.5	Surface	1.0	0.1	222	15.1	15.1	8.3	8.3	31.9	31.9	104.8	105.0	8.3	8.6	5.0	4.7	7	-	5	-	817203	807791	-	-	-					
						1.0	0.1	223	15.1		15.1		8.3		31.9		105.1		8.7		5.1	6		-			-	-	-					
					Middle	4.3	0.0	217	15.0	15.0	8.2	8.2	31.9	32.0	103.9	104.1	8.6	8.8	3.3	5.9	5	-	-	-			-	-	-	-				
						4.3	-	222	15.0	15.0	8.2		32.0		104.2		8.6		3.6		5	-	-	-			-							
					Bottom	7.5	0.0	225	15.2	15.2	8.3	8.3	32.3	32.2	106																			

Expansion of Hong Kong International Airport into a Three-Runway System
Water Quality Monitoring
Water Quality Monitoring Results on 26 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)								
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA			
C1	Fine	Rough	21:39	8.2	Surface	1.0	0.5	217	15.2	15.2	8.1	8.1	31.1	31.3	102.1	102.3	8.5	8.6	4.3	7.5	2	4	86	89	815635	804241	<0.2	<0.2	0.5	0.5							
						1.0	0.5	210	15.2		8.1	8.1	31.4	31.3	102.5	104.4	8.5		3.9		3		85				<0.2		0.6								
					Middle	4.1	0.5	191	15.5	15.5	8.1	8.1	32.2	32.3	104.4	104.5	8.6	8.4	9.9	4	89	<0.2	0.5														
						4.1	0.5	196	15.5		8.1	8.1	32.3	32.6	104.5	102.6	8.6		10.1		4	89	<0.2	0.5													
					Bottom	7.2	0.5	208	15.5	15.5	8.5	8.5	32.6	32.5	102.4	102.7	8.4	8.4	8.1	5	91	<0.2	0.5														
						7.2	0.5	210	15.5		8.5	8.5	32.4	32.5	102.7	104.2	8.4		8.4		5	92	<0.2	0.5													
					C2	Fine	Rough	20:11	10.2	Surface	1.0	0.3	173	15.3	15.3	8.1	8.1	30.9	31.0	98.9	99.0	8.2	8.1	3.9			3.9	5	5	87	90	825683	806941	<0.2	<0.2	0.6	0.5
											1.0	0.3	176	15.3		8.1	8.1	31.1	31.0	99.0	97.6	8.2		4.4				5		87				<0.2		0.5	
Middle	5.1	0.4	180	15.6						15.6	8.2	8.2	31.5	31.7	97.7	97.5	8.1	8.5	3.1	4	89	<0.2	0.5														
	5.1	0.3	179	15.6							8.2	8.2	31.8	31.6	97.5	104.1	8.0		3.3		5	90	<0.2	0.5													
Bottom	9.2	0.3	168	15.7						15.7	8.3	8.3	31.6	31.6	103.9	104.2	8.5	8.5	4.4	5	92	<0.2	0.4														
	9.2	0.4	172	15.7							8.3	8.3	31.6	31.6	104.2	104.1	8.5		4.0		4	92	<0.2	0.5													
C3	Fine	Rough	21:57	11.0						Surface	1.0	0.4	84	15.7	15.7	8.2	8.3	31.7	31.7	92.2	92.9	7.5	7.7	1.2	1.7	6	6	84	88	822113	817819			<0.2	<0.2	0.6	0.5
											1.0	0.5	79	15.7		8.4	8.3	31.6	31.7	93.5	93.9	7.7		1.3		6		84						<0.2		0.5	
					Middle	5.5	0.4	84	15.7	15.7	8.4	8.3	31.6	31.7	93.6	94.1	7.7	7.7	2.0	6	87	<0.2	0.5														
						5.5	0.4	88	15.7		8.2	8.3	31.8	31.8	94.1	94.1	7.7		1.9		6	88	<0.2	0.4													
					Bottom	10.0	0.4	94	15.7	15.6	8.2	8.2	31.8	31.8	93.9	94.2	7.7	7.7	2.0	6	91	<0.2	0.4														
						10.0	0.4	93	15.5		8.2	8.2	31.8	31.8	94.2	94.1	7.7		1.8		6	92	<0.2	0.5													
					IM1	Fine	Rough	21:23	6.1	Surface	1.0	0.3	206	15.1	15.1	8.3	8.3	31.3	31.6	105.5	105.3	8.6	8.6	3.0	4.2	3	4	86	88			818327	806450	<0.2	<0.2	0.4	0.5
											1.0	0.4	204	15.1		8.3	8.3	31.8	31.6	105.0	103.4	8.7		3.4		4		87						<0.2		0.5	
Middle	3.1	0.4	178	15.2						15.2	8.1	8.1	31.9	32.1	103.1	103.6	8.5	8.6	4.9	5.1	3	4	87	<0.2	0.4												
	3.1	0.4	178	15.2							8.1	8.1	32.3	32.3	103.6	101.7	8.6		5.1		4		87	<0.2	0.5												
Bottom	5.1	0.3	200	15.3						15.3	8.3	8.3	32.3	32.3	101.6	101.7	8.4	8.4	4.6	5	90	<0.2	0.5														
	5.1	0.3	204	15.3							8.3	8.3	32.3	32.3	101.7	101.7	8.4		4.2		5	89	<0.2	0.5													
IM2	Fine	Rough	21:11	6.5						Surface	1.0	0.4	208	15.0	15.0	8.2	8.2	31.7	31.8	100.4	100.5	8.3	8.3	4.3	5.3	4	4	85	88	819192	806262			<0.2	<0.2	0.4	0.4
											1.0	0.3	202	15.0		8.2	8.2	31.9	31.8	100.6	100.0	8.4		4.7		4		85						<0.2		0.4	
					Middle	3.3	0.3	177	15.4	15.4	8.0	8.0	32.0	32.2	100.1	99.8	8.3	8.5	6.0	6.3	3	4	88	<0.2	0.4												
						3.3	0.4	173	15.4		8.0	8.0	32.3	32.2	100.1	103.9	8.2		5.5		3		89	<0.2	0.4												
					Bottom	5.5	0.3	174	15.2	15.2	8.0	8.0	32.2	32.2	103.9	103.7	8.5	8.5	5.5	5.1	4	4	90	<0.2	0.5												
						5.5	0.3	167	15.2		8.0	8.0	32.2	32.2	103.7	103.8	8.5		5.1		4		90	<0.2	0.5												
IM7	Fine	Rough	20:41	7.0	Surface	1.0	0.2	157	15.2	15.2	8.2	8.2	32.0	32.1	100.8	101.0	8.3	8.4	4.9	4.5	4	6	85	88	821373	806850	<0.2	<0.2	0.4	0.5							
						1.0	0.2	158	15.2		8.2	8.2	32.1	32.1	101.1	101.9	8.3		5.0		6		85				<0.2		0.6								
					Middle	3.5	0.2	148	15.3	15.3	8.2	8.2	31.9	32.0	101.9	101.8	8.4	8.8	3.6	4.8	6	6	88	<0.2			0.5										
						3.5	0.2	143	15.3		8.2	8.2	32.0	32.1	101.8	106.4	8.4		3.8		6		88	<0.2			0.4										
					Bottom	6.0	0.2	158	15.3	15.3	8.2	8.2	32.1	32.1	106.4	106.3	8.8	8.8	4.8	4.7	6	5	90	<0.2			0.5										
						6.0	0.2	160	15.3		8.2	8.2	32.1	32.1	106.1	106.3	8.7		4.7		5		91	<0.2			0.4										

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

Expansion of Hong Kong International Airport into a Three-Runway System
Water Quality Monitoring
Water Quality Monitoring Results on 26 February 22 during Mid-Ebb Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)				
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value
IM10	Fine	Rough	20:12	8.2	Surface	1.0	0.3	117	15.4	15.5	8.2	8.2	31.4	31.4	95.2	94.0	7.9	7.7	4.6	3.5	6	6	85	89	822248	809814	<0.2	<0.2	0.4	0.5			
						1.0	0.3	121	15.6		8.2		31.3		92.7		7.6		4.0		6		86				<0.2		0.4				
					Middle	4.1	0.4	95	15.6	15.4	8.2	8.3	31.5	31.4	93.1	92.2	7.7	3.5	6	5	89	90	<0.2	0.6									
						4.1	0.4	92	15.2		8.3		31.2		91.3		7.5		3.2		5		90	<0.2			0.4						
					Bottom	7.2	0.3	115	15.2	15.3	8.3	4.1	31.4	31.4	91.3	91.3	7.6	7.7	6.4	4	91	91	<0.2	0.5									
						7.2	0.3	113	15.4		-0.2		31.3		91.2		7.7		-0.5		4		91	<0.2			0.5						
IM11	Fine	Rough	20:28	8.3	Surface	1.0	0.4	89	15.4	15.5	8.1	8.2	31.2	31.3	90.0	90.5	7.4	7.6	1.8	2.6	8	6	83	89	821489	810555	<0.2	<0.2	0.4	0.5			
						1.0	0.4	83	15.5		8.2		31.3		91.0		7.5		2.0		6		84				<0.2		0.5				
					Middle	4.2	0.5	108	15.5	15.5	8.2	8.2	31.6	31.6	90.7	92.5	7.5	7.8	1.6	4	5	6	90	91			<0.2		0.5				
						4.2	0.5	107	15.4		8.2		31.5		94.3		7.8		1.7		6		91				<0.2		0.5				
					Bottom	7.3	0.5	114	15.4	15.4	8.2	8.2	31.5	31.5	94.1	94.6	7.8	7.8	4.0	4	92	96	<0.2	0.4									
						7.3	0.4	116	15.4		8.2		31.4		95.1		7.8		4.2		4		96	<0.2			0.5						
IM12	Fine	Rough	20:37	9.4	Surface	1.0	0.4	85	15.7	15.7	8.1	8.1	31.3	31.3	93.2	92.6	7.6	7.6	2.4	2.8	4	5	85	88	821152	811529	<0.2	<0.2	0.5	0.5			
						1.0	0.4	79	15.7		8.0		31.3		91.9		7.5		2.5		6		85				<0.2		0.5				
					Middle	4.7	0.4	112	15.7	15.7	8.0	8.2	31.5	31.5	91.6	92.2	7.5	7.6	3.4	5	86	89	<0.2	0.4									
						4.7	0.5	117	15.6		8.4		31.4		92.8		7.6		3.5		5		89	<0.2			0.5						
					Bottom	8.4	0.5	112	15.6	15.5	8.4	8.3	31.5	31.4	93.2	91.7	7.7	7.6	2.6	4	91	91	<0.2	0.5									
						8.4	0.5	108	15.4		8.1		31.3		90.2		7.4		2.6		4		91	<0.2			0.5						
SR1A	Fine	Moderate	21:10	4.8	Surface	1.0	0.0	68	15.1	15.1	8.2	8.3	30.5	30.6	91.4	91.1	7.6	7.6	4.0	3.8	6	5	-	-	819972	812662	-	-	-	-			
						1.0	0.0	61	15.1		8.4		30.6		90.8		7.6		4.3		5		-				-		-				
					Middle	2.4	0.0	51	-	-	-	-	-	-	-	-	-	-	-	-	-	5	-	-			-		-		-	-	-
						2.4	0.0	49	-		-		-		-		-		-		-		-				-		-		-	-	-
					Bottom	3.8	-	47	15.1	15.3	8.4	8.3	30.9	30.8	91.0	91.6	7.6	7.7	3.5	4	-	5	-	-			-		-		-	-	-
						3.8	0.0	39	15.5		8.2		30.6		92.1		7.7		3.3		5		-				-		-				
SR2	Fine	Moderate	21:26	5.1	Surface	1.0	0.6	36	15.5	15.6	8.2	8.3	31.6	31.6	93.8	95.2	7.7	7.8	1.4	1.7	4	4	89	91	821448	814163	<0.2	<0.2	0.5	0.5			
						1.0	0.6	38	15.7		8.4		31.6		96.6		7.9		1.5		4		90				<0.2		0.5				
					Middle	-	0.5	25	-	-	-	-	-	-	-	-	-	-	-	-	-	4	-	-			-		-		-	-	-
						-	0.5	26	-		-		-		-		-		-		-		-				-		-		-	-	-
					Bottom	4.1	0.6	24	15.7	15.4	8.4	8.3	31.5	31.6	96.2	94.0	7.9	7.7	2.0	3	91	92	<0.2	0.4									
						4.1	0.5	28	15.1		8.2		31.7		91.7		7.5		1.8		4		92	<0.2			0.4						
SR3	Fine	Rough	20:35	8.3	Surface	1.0	0.3	158	15.3	15.3	8.2	8.2	31.8	31.7	103.0	103.3	8.5	8.6	4.9	5.1	6	5	-	-	822143	807569	-	-	-	-			
						1.0	0.4	162	15.3		8.2		31.6		103.5		8.5		4.9		5		-				-		-				
					Middle	4.2	0.3	151	15.3	15.3	8.1	8.1	31.8	31.8	104.1	104.0	8.6	8.6	5.9	4	-	5	-	-			-		-		-	-	
						4.2	0.3	154	15.3		8.1		31.8		103.8		8.6		6.0		4		-				-		-				
					Bottom	7.3	0.4	166	15.3	15.3	8.3	8.3	31.9	31.9	101.4	101.4	8.4	8.4	4.3	5	-	5	-	-			-		-		-	-	
						7.3	0.4	160	15.3		8.3		31.8		101.4		8.4		4.3		5		-				-		-				
SR4A	Fine	Rough	21:59	8.3	Surface	1.0	0.0	75	15.0	15.0	8.1	8.1	32.0	31.9	104.4	104.6	8.8	8.8	3.9	4.7	6	6	-	-	817202	807783	-	-	-	-			
						1.0	0.0	70	15.0		8.1		31.7		104.8		8.7		4.0		6		-				-		-				
					Middle	4.2	0.1	73	15.0	15.0	8.0	8.0	32.0	32.0	105.7	105.8	8.8	8.8	2.9	5	-	6	-	-			-		-		-	-	
						4.2	0.1	70	15.0		8.0		32.0		105.9		8.8		3.2		5		-				-		-				
					Bottom	7.3	0.0	46	14.9	14.9	8.1	8.1	32.2	32.3	104.9	104.9	8.7	8.7	7.1	5	-	5	-	-			-		-		-	-	
						7.3	0.0	48	14.9		8.1		32.3		104.8		8.7		6.8		5		-				-		-				
SR8	Fine	Moderate	20:49	5.2	Surface	1.0	-	-	15.5	15.4	8.2	8.2	30.7	30.9	92.5	93.9	7.7	7.8	2.8	2.5	6	5	-	-	820374	811614	-	-	-	-			
						1.0	-	-	15.3		8.2		31.0		95.3		7.9		2.7		5		-				-		-				
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	5	-	-			-		-		-	-	-
						-	-	-	-		-		-		-		-		-		-		-				-		-		-	-	-
					Bottom	4.2	-	-	15.3	15.5	8.2	8.2	31.4	31.4	95.0	94.0	7.9	7.8	2.2	4	-	3	-	-			-		-		-	-	-
						4.2	-	-	15.7		8.1		31.3		93.0		7.7		2.1		3		-				-		-				

Expansion of Hong Kong International Airport into a Three-Runway System

Water Quality Monitoring

Water Quality Monitoring Results on 26 February 22 during Mid-Flood Tide

Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)	
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA
C1	Fine	Rough	07:57	8.5	Surface	1.0	0.1	37	15.2	15.2	8.1	8.1	31.4	31.4	107.6	107.7	8.9	8.8	6.1	8.4	4	5	85	89	815612	804233	<0.2	<0.2	0.4	0.4
						1.0	0.1	36	15.2	15.2	8.1	8.1	31.4	31.4	107.7	107.7	8.9	8.8	6.4	8.4	4	5	86	89			<0.2	<0.2	0.5	0.5
					Middle	4.3	0.1	37	15.2	15.2	8.2	8.2	32.0	32.1	104.9	104.8	8.7	8.6	9.7	8.4	4	5	89	91			<0.2	<0.2	0.4	0.4
						4.3	0.1	35	15.2	15.2	8.2	8.2	32.2	32.2	104.7	104.7	8.6	8.6	9.2	8.4	5	6	89	91			<0.2	<0.2	0.4	0.4
					Bottom	7.5	0.1	28	15.3	15.3	8.4	8.4	32.5	32.4	104.7	104.9	8.6	8.6	9.3	8.6	6	6	91	92			<0.2	<0.2	0.4	0.4
						7.5	0.1	35	15.3	15.3	8.4	8.4	32.2	32.2	105.1	105.1	8.6	8.6	9.4	8.6	5	6	92	92			<0.2	<0.2	0.5	0.5
					Surface	1.0	0.0	179	15.4	15.4	8.2	8.2	31.0	30.9	99.6	99.6	8.1	8.3	4.0	3.9	4	5	86	89	825691	806931	<0.2	<0.2	0.4	0.4
						1.0	0.1	171	15.4	15.4	8.2	8.2	30.8	30.9	99.2	99.2	8.2	8.3	4.2	3.9	3	5	87	89			<0.2	<0.2	0.4	0.4
C2	Fine	Rough	09:14	10.4	Middle	5.2	0.1	184	15.9	15.9	8.3	8.3	31.6	31.7	102.1	102.2	8.5	8.3	3.9	3.7	5	6	89	90			<0.2	<0.2	0.5	0.5
						5.2	0.1	188	15.9	15.9	8.3	8.3	31.8	31.7	102.2	102.2	8.3	8.3	3.7	3.7	4	5	90	91			<0.2	<0.2	0.5	0.5
					Bottom	9.4	0.0	197	16.2	16.2	8.0	8.0	31.9	31.8	102.1	102.1	8.3	8.3	3.6	3.7	5	6	91	92			<0.2	<0.2	0.4	0.4
						9.4	0.1	191	16.2	16.2	8.0	8.0	31.6	31.8	102.0	102.0	8.3	8.3	3.7	3.7	6	6	92	92			<0.2	<0.2	0.4	0.4
C3	Fine	Rough	08:36	11.1	Surface	1.0	0.1	152	15.7	15.7	8.0	8.0	31.4	31.6	90.5	90.6	7.5	7.4	1.4	1.5	6	6	85	86	822089	817782	<0.2	<0.2	0.5	0.4
						1.0	0.1	154	15.7	15.7	8.0	8.0	31.7	31.6	90.7	90.7	7.4	7.4	1.5	1.5	6	6	86	86			<0.2	<0.2	0.4	0.4
					Middle	5.6	0.1	157	15.8	15.8	8.2	8.2	32.0	31.9	93.2	93.2	7.6	7.6	8.2	8.2	5	4	90	89			<0.2	<0.2	0.4	0.4
						5.6	0.1	156	15.8	15.8	8.2	8.2	31.8	31.8	93.2	93.2	7.6	7.6	8.2	8.2	4	5	89	91			<0.2	<0.2	0.4	0.4
					Bottom	10.1	0.0	161	15.9	15.9	8.0	8.0	31.9	31.8	90.8	90.7	7.4	7.4	7.1	7.3	6	5	91	92			<0.2	<0.2	0.5	0.4
						10.1	0.0	161	15.9	15.9	8.0	8.0	31.6	31.6	90.6	90.6	7.4	7.4	7.3	7.3	5	5	92	92			<0.2	<0.2	0.4	0.4
IM1	Fine	Moderate	08:18	6.6	Surface	1.0	0.0	12	15.2	15.2	8.2	8.2	32.2	32.3	104.0	103.9	8.6	8.7	6.1	6.4	4	4	87	86	818348	806458	<0.2	<0.2	0.5	0.5
						1.0	0.1	12	15.2	15.2	8.2	8.2	32.3	32.3	103.7	103.7	8.5	8.5	6.4	6.5	4	4	86	88			<0.2	<0.2	0.5	0.5
					Middle	3.3	0.1	36	15.2	15.2	8.2	8.2	32.5	32.3	107.1	107.4	8.8	8.4	6.5	6.8	6	5	88	88			<0.2	<0.2	0.5	0.5
						3.3	0.1	42	15.2	15.2	8.2	8.2	32.1	32.3	107.6	107.6	8.9	8.4	6.8	6.8	5	4	88	90			<0.2	<0.2	0.5	0.5
					Bottom	5.6	0.1	5	15.2	15.2	8.3	8.3	32.2	32.3	101.9	101.8	8.4	8.4	9.6	9.1	4	3	90	91			<0.2	<0.2	0.5	0.5
						5.6	0.1	7	15.2	15.2	8.3	8.3	32.4	32.3	101.6	101.6	8.4	8.4	9.1	9.1	3	3	91	91			<0.2	<0.2	0.5	0.5
IM2	Fine	Rough	08:25	7.2	Surface	1.0	0.1	31	15.1	15.1	8.3	8.3	31.7	31.7	101.0	101.0	8.2	8.4	4.8	4.4	4	4	85	85	819161	806219	<0.2	<0.2	0.5	0.4
						1.0	0.1	31	15.1	15.1	8.3	8.3	31.7	31.7	100.9	100.9	8.4	8.4	4.4	4.4	4	4	85	85			<0.2	<0.2	0.4	0.4
					Middle	3.6	0.1	30	15.0	15.0	8.0	8.0	31.8	31.8	104.9	105.1	8.7	8.3	5.1	5.1	4	3	88	88			<0.2	<0.2	0.4	0.4
						3.6	0.1	27	15.0	15.0	8.0	8.0	31.8	31.8	105.3	105.3	8.7	8.3	5.1	5.1	3	5	88	91			<0.2	<0.2	0.4	0.4
					Bottom	6.2	0.1	7	15.1	15.1	8.2	8.2	32.0	32.2	100.4	100.5	8.3	8.3	7.0	7.2	5	5	91	91			<0.2	<0.2	0.5	0.4
						6.2	0.1	14	15.1	15.1	8.2	8.2	32.3	32.2	100.5	100.5	8.3	8.3	7.2	7.2	5	5	91	91			<0.2	<0.2	0.4	0.4
IM7	Fine	Moderate	08:47	7.7	Surface	1.0	0.1	83	15.9	15.9	8.1	8.1	31.6	31.7	99.1	99.1	8.1	8.3	4.6	4.3	5	7	85	85	821332	806817	<0.2	<0.2	0.4	0.4
						1.0	0.1	78	15.9	15.9	8.1	8.1	31.8	31.7	99.1	99.1	8.1	8.3	4.3	4.0	6	6	85	88			<0.2	<0.2	0.5	0.5
					Middle	3.9	0.1	78	15.6	15.6	8.4	8.4	31.7	31.8	102.5	102.7	8.4	8.6	4.0	3.9	6	6	88	88			<0.2	<0.2	0.4	0.4
						3.9	0.0	74	15.6	15.6	8.4	8.4	31.9	31.7	102.9	102.9	8.4	8.6	3.9	3.0	6	6	88	91			<0.2	<0.2	0.4	0.4
					Bottom	6.7	0.1	84	15.8	15.8	8.2	8.2	31.7	31.9	104.5	104.3	8.6	8.6	3.0	3.3	6	4	91	90			<0.2	<0.2	0.5	0.5
						6.7	0.1	83	15.8	15.8	8.2	8.2	32.0	31.9	104.1	104.1	8.5	8.6	3.3	3.3	4	4	90	90			<0.2	<0.2	0.5	0.5

DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**




Expansion of Hong Kong International Airport into a Three-Runway System




Water Quality Monitoring




Water Quality Monitoring Results on 26 February 22 during Mid-Flood Tide




Monitoring Station	Weather Condition	Sea Condition	Sampling Time	Water Depth (m)	Sampling Depth (m)		Current Speed (m/s)	Current Direction	Water Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen		Turbidity(NTU)		Suspended Solids (mg/L)		Total Alkalinity		Coordinate HK Grid (Northing)	Coordinate HK Grid (Easting)	Chromium (µg/L)		Nickel (µg/L)										
									Value	Average	Value	Average	Value	Average	Value	Average	Value	DA	Value	DA	Value	DA	Value	DA			Value	DA	Value	DA	Value	DA	Value	DA					
IM10	Fine	Rough	10:44	8.4	Surface	1.0	0.1	125	15.0	15.0	8.2	8.2	31.0	31.0	93.4	93.3	7.7	7.8	1.9	3.3	6	6	85	89	822248	809837	<0.2	<0.2	0.5	0.5									
						1.0	0.1	121	15.0		8.2	31.0	93.1	7.8	1.7	5	86		<0.2		0.5																		
					Middle	4.2	0.1	131	15.0	15.0	8.2	8.2	31.4	31.3	93.5	93.7	7.8	2.9	7	89	<0.2	0.5																	
						4.2	0.1	129	15.0		8.2	31.2	93.9	7.8	2.8	5	90	<0.2	0.5																				
					Bottom	7.4	0.1	140	15.0	15.0	8.0	8.0	31.1	31.2	96.3	96.2	8.0	5.3	6	92	<0.2	0.5																	
						7.4	0.1	132	15.0		8.0	31.3	31.2	96.1	8.0	8.0	5.1	7	92	<0.2	0.5																		
					IM11	Fine	Rough	10:17	8.8	Surface	1.0	0.1	93	15.2	15.2	8.1	8.1	31.3	31.4	91.5	91.6	7.6	7.6	5.6			8.6		3		5	86	88	821500	810558	<0.2	<0.2	0.4	0.4
											1.0	0.0	89	15.2		8.1	31.4	91.6	7.6	5.7	3	86		<0.2					0.4										
Middle	4.4	0.1	102	15.3						15.3	8.2	8.2	31.1	31.3	92.1	92.1	7.6	9.5	5	89	<0.2	0.5																	
	4.4	0.1	103	15.3							8.2	31.5	92.0	7.6	9.2	6	89	<0.2	0.4																				
Bottom	7.8	0.1	86	15.3						15.3	8.2	8.2	31.2	31.2	95.4	95.3	7.9	10.8	5	90	<0.2	0.5																	
	7.8	0.1	92	15.3							8.2	31.1	31.2	95.1	7.9	7.9	10.5	6	90	<0.2	0.4																		
IM12	Fine	Rough	09:59	9.6						Surface	1.0	0.1	90	15.4	15.4	8.2	8.2	31.2	31.3	95.2	95.1	7.9	7.8	4.5	5.1	6	5	85	89	821163	811513	<0.2	<0.2			0.5		0.4	
											1.0	0.1	91	15.4		8.2	31.4	95.0	7.8	4.2	4	86		<0.2		0.4													
					Middle	4.8	0.1	85	15.6	15.6	8.2	8.2	31.4	31.4	94.9	95.0	7.8	5.4	5	89	<0.2	0.5																	
						4.8	0.1	86	15.6		8.2	31.3	95.0	7.8	5.1	4	90	<0.2	0.4																				
					Bottom	8.6	0.1	90	15.3	15.3	8.1	8.1	31.2	31.3	95.0	94.8	7.8	5.7	6	92	<0.2	0.4																	
						8.6	0.1	94	15.3		8.1	31.3	31.3	94.6	7.8	7.8	5.8	6	92	<0.2	0.4																		
					SR1A	Fine	Moderate	09:16	4.8	Surface	1.0	0.0	123	15.0	15.0	8.2	8.2	30.8	30.7	93.1	92.9	7.7	7.7	4.2	3.8	6	4	-	-			819968		812659	-	-	-		-
											1.0	0.0	119	15.0		8.2	30.6	92.6	7.7	4.1	4	-		-		-													
Middle	2.4	0.0	143	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-									
	2.4	0.0	144	-							-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-										
Bottom	3.8	0.0	127	15.2						15.2	8.2	8.2	30.6	30.7	91.2	91.2	7.6	3.2	4	-	-	-	-	-	-	-	-	-	-	-									
	3.8	0.1	129	15.2							8.2	30.8	30.7	91.1	7.6	7.6	3.6	3	-	-	-	-	-	-	-	-	-	-	-										
SR2	Fine	Moderate	09:01	5.2						Surface	1.0	0.0	124	15.4	15.4	8.1	8.1	31.5	31.5	95.4	95.2	7.9	7.9	1.0	1.5	6	6	88	90	821446	814157		<0.2		<0.2		0.4	0.4	
											1.0	0.0	128	15.4		8.1	31.4	95.0	7.8	1.0	6	89		<0.2		0.4													
					Middle	-	0.1	102	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-							
						-	0.1	102	-		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			-							
					Bottom	4.2	0.0	131	15.5	15.5	8.4	8.4	31.5	31.4	98.3	98.1	8.1	2.1	5	-	-	-	-	-	-	-	-	-	-			-							
						4.2	0.0	133	15.5		8.4	31.3	31.4	97.8	8.0	8.1	2.0	7	91	<0.2	0.5																		
					SR3	Fine	Moderate	08:55	8.8	Surface	1.0	0.1	106	15.6	15.6	8.2	8.2	31.7	31.7	99.0	99.2	8.0	8.4	3.2	2.4	5	5	-	-			822144	807553	-		-	-		-
											1.0	0.0	108	15.6		8.2	31.6	99.3	8.1	3.3	4	-		-		-													
Middle	4.4	0.1	83	15.7						15.7	8.2	8.2	31.7	31.7	105.5	105.8	8.7	1.8	4	-	-	-	-	-	-	-	-	-	-	-									
	4.4	0.1	80	15.7							8.2	31.7	105.8	8.7	2.0	4	-	-	-	-	-	-	-	-	-	-	-	-											
Bottom	7.8	0.0	114	15.9						15.9	8.1	8.1	31.8	31.9	103.1	103.1	8.4	1.8	6	-	-	-	-	-	-	-	-	-	-	-									
	7.8	0.0	118	15.9							8.1	32.0	103.0	8.4	2.0	8	-	-	-	-	-	-	-	-	-	-	-	-											
SR4A	Fine	Rough	07:34	8.7						Surface	1.0	0.0	273	15.5	15.5	8.2	8.2	31.1	30.9	104.4	104.6	8.6	8.4	5.1	5.3	7	7	-	-	817173	807789			-	-		-	-	
											1.0	0.0	266	15.5		8.2	30.7	104.8	8.6	4.9	7	-		-		-													
					Middle	4.4	0.0	292	15.1	15.1	8.3	8.3	31.0	31.1	97.9	98.1	8.1	5.1	7	-	-	-	-	-	-	-	-	-	-			-							
						4.4	0.0	286	15.1		8.3	31.2	98.3	8.2	5.0	7	-	-	-	-	-	-	-	-	-	-	-	-	-										
					Bottom	7.7	0.0	286	15.3	15.3	8.3	8.3	32.0	32.1	101.8	102.0	8.5	5.7	6	-	-	-	-	-	-	-	-	-	-			-							
						7.7	0.0	289	15.3		8.3	32.2	102.2	8.4	6.0	6	-	-	-	-	-	-	-	-	-	-	-	-	-										
					SR8	Fine	Moderate	09:44	5.7	Surface	1.0	-	-	15.2	15.2	8.2	8.2	31.3	31.3	94.5	94.7	7.8	7.9	4.1	3.2	6	6	-	-			820388	811608	-		-	-		-
											1.0	-	-	15.2		8.2	31.2	31.3	94.9	7.9	3.6	5		-		-		-											
Middle	-	-	-	-						-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-								
	-	-	-	-							-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-									
Bottom	4.7	-	-	15.3						15.3	8.2	8.2	31.1	31.2	91.7	91.5	7.6	7.6	2.3	5	-	-	-	-	-	-	-	-	-	-	-								
	4.7	-	-	15.3							8.2	31.3	31.2	91.3	7.6	7.6	2.6	6	-	-	-	-	-	-	-	-	-	-	-										




DA: Depth-Averaged
Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher
Value exceeding Action Level is underlined; **Value exceeding Limit Level is bolded and underlined**

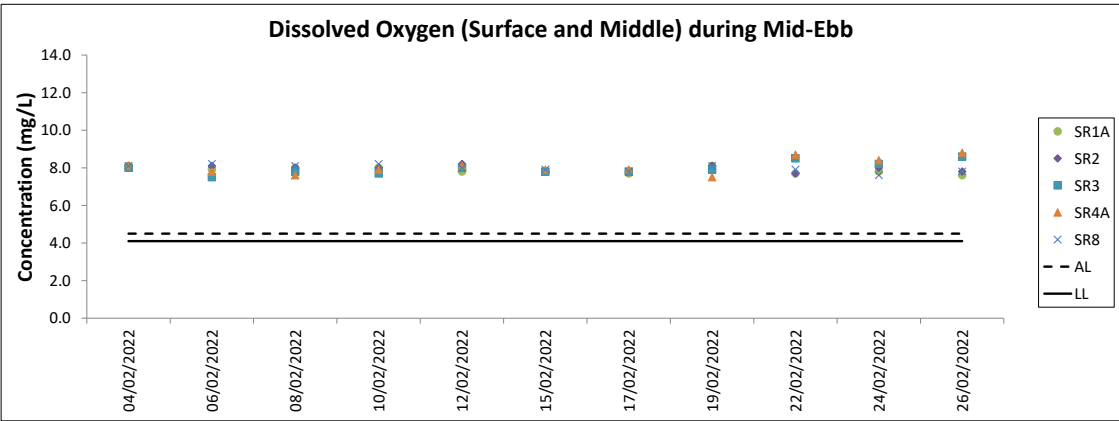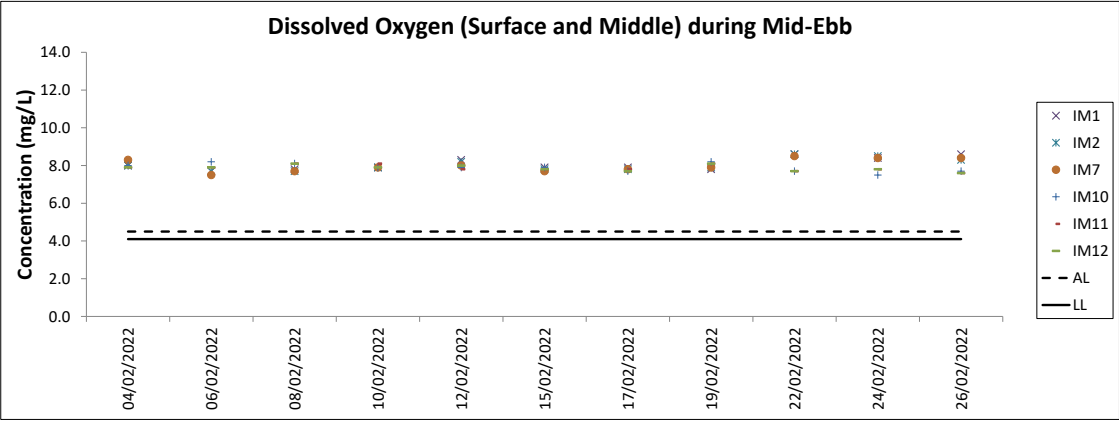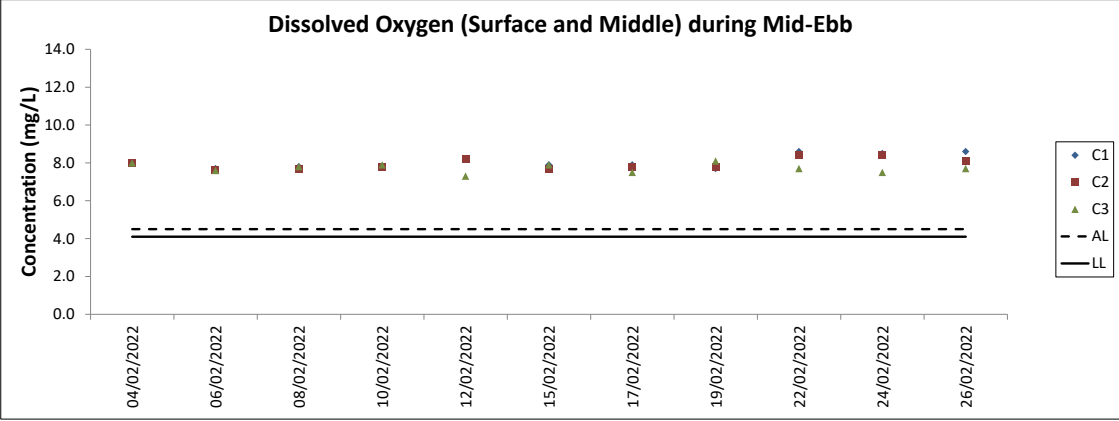

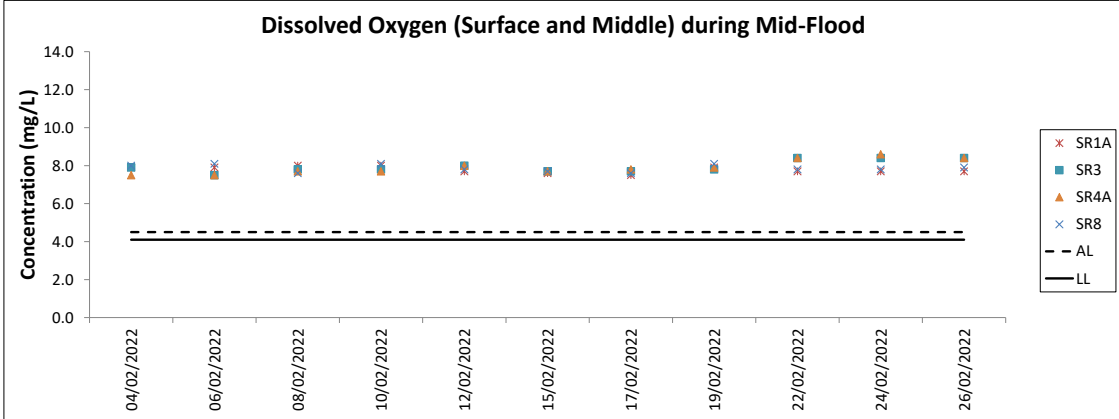
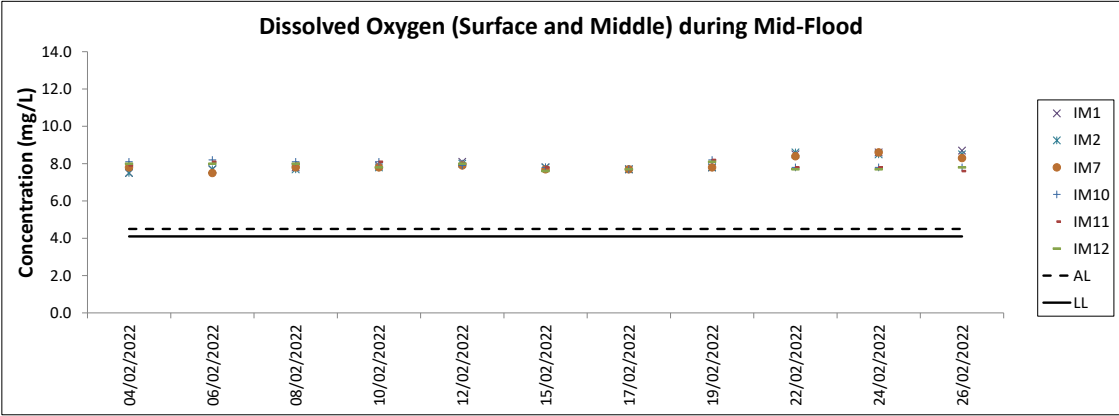
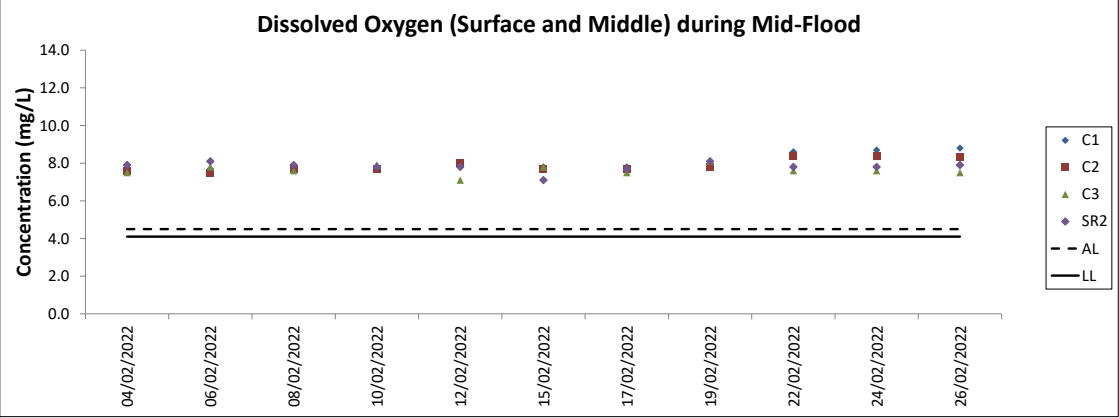


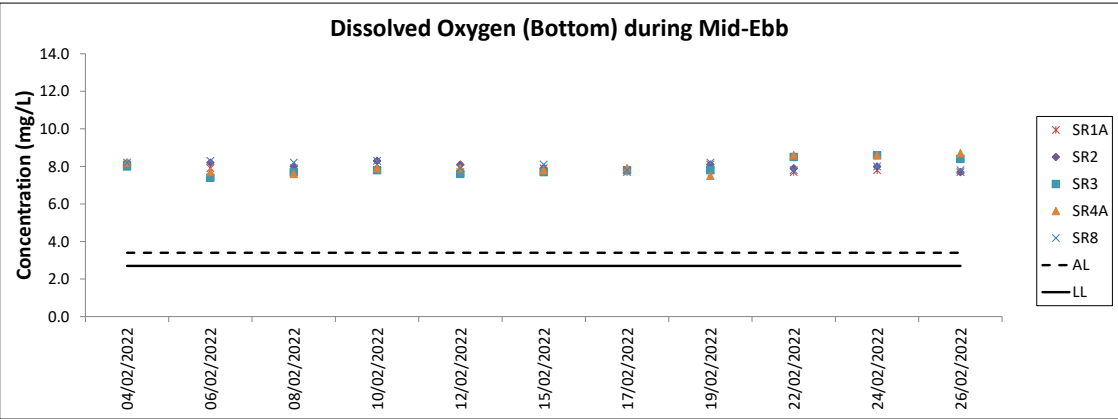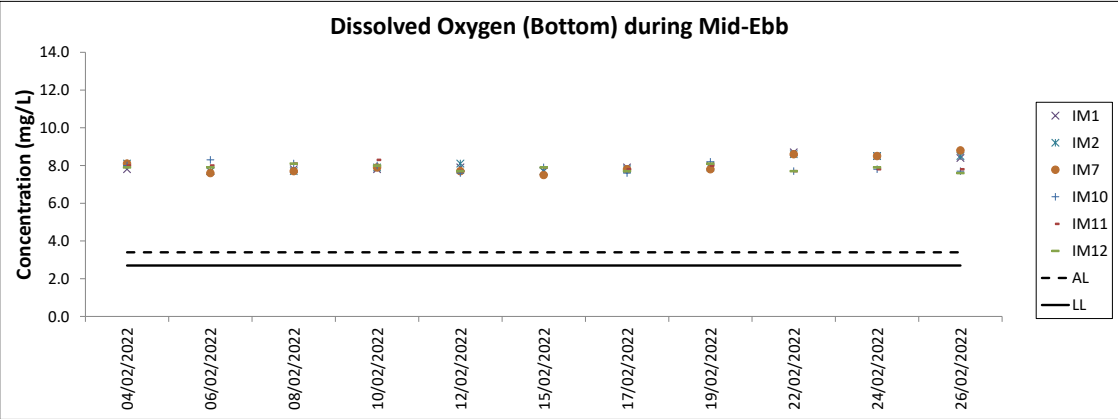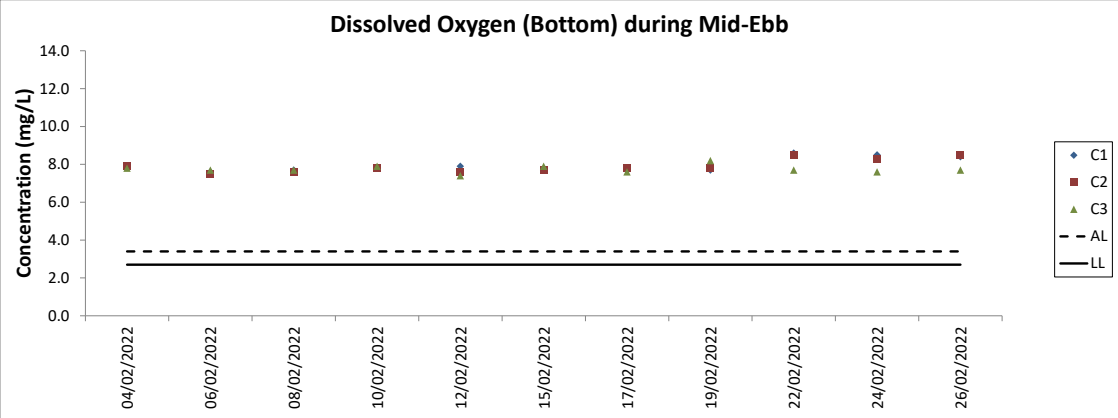

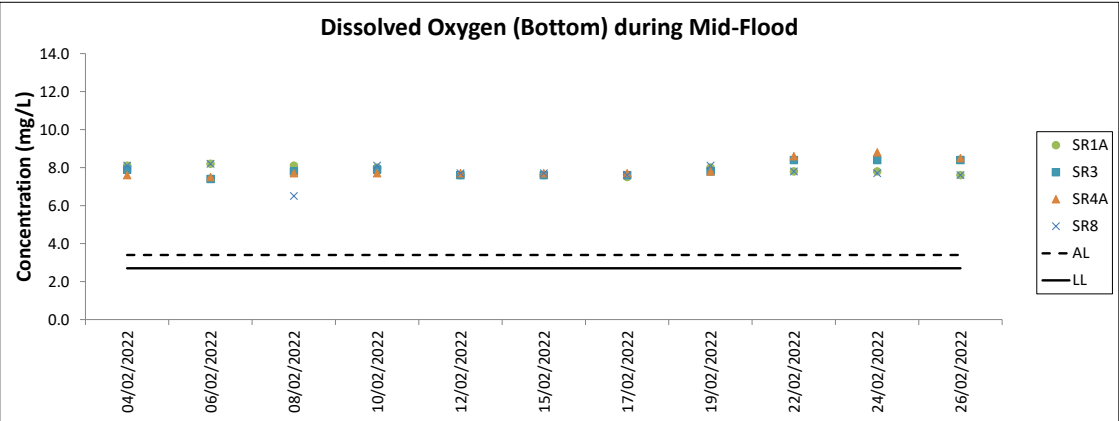
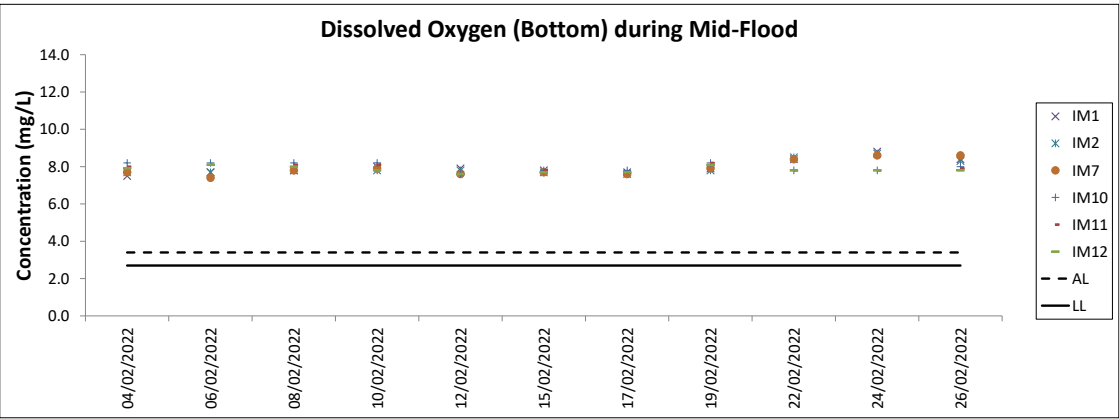
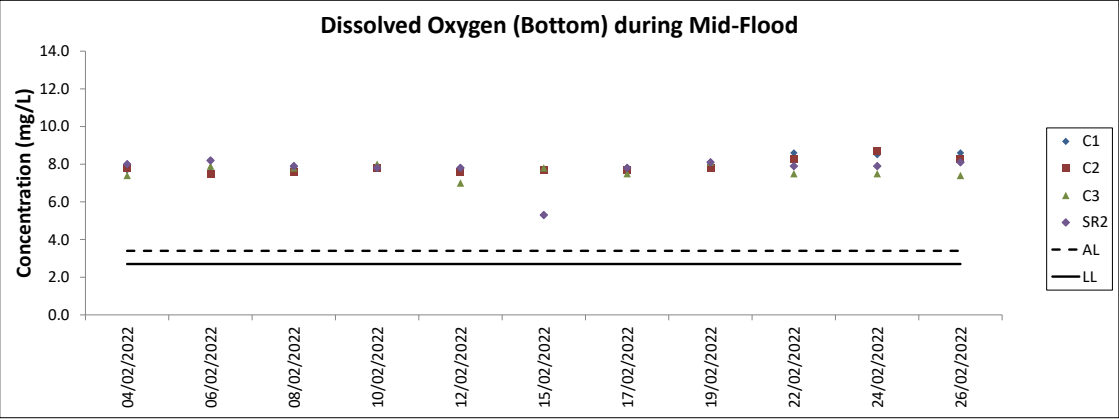


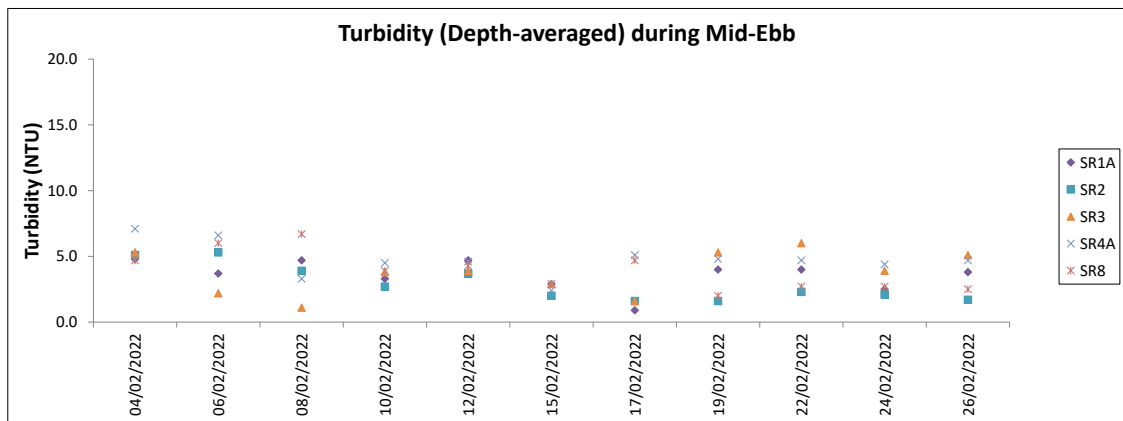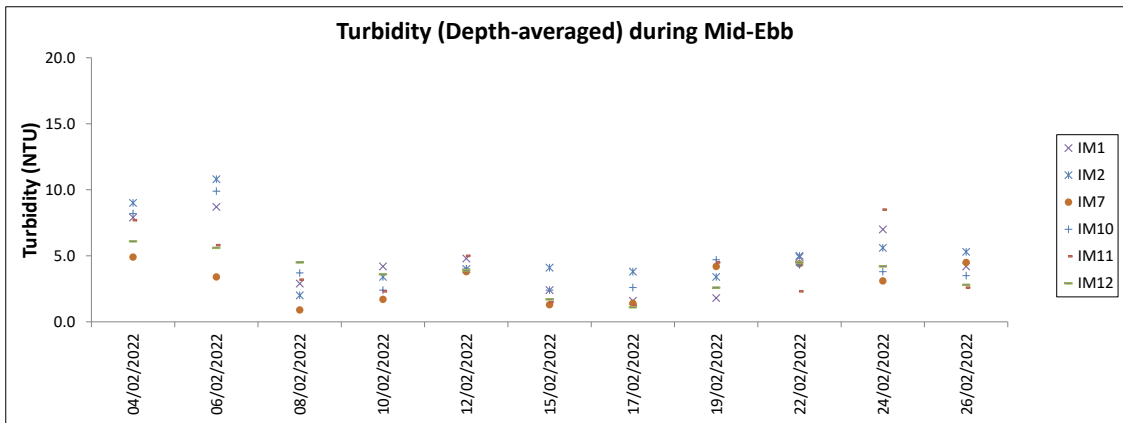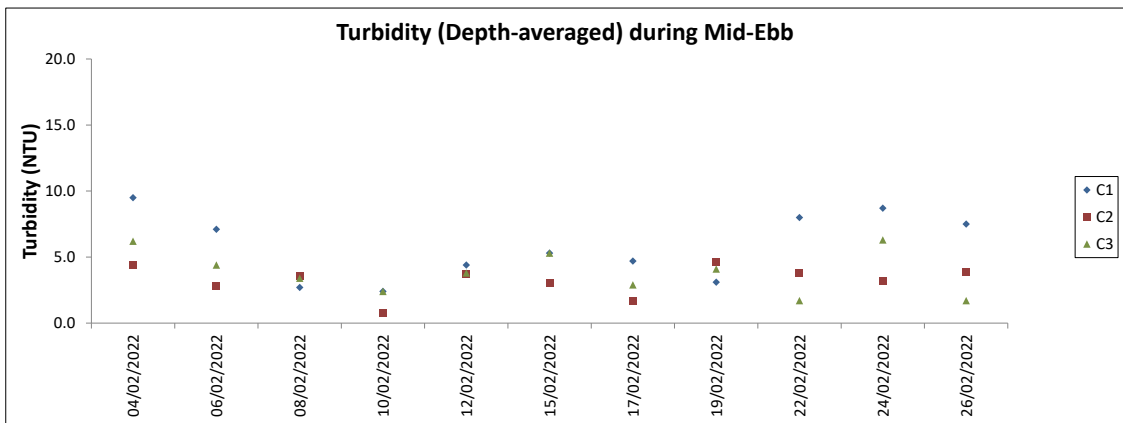




Note: The Action and Limit Level of turbidity can be referred to Table 4.2 of the monthly EM&A report.

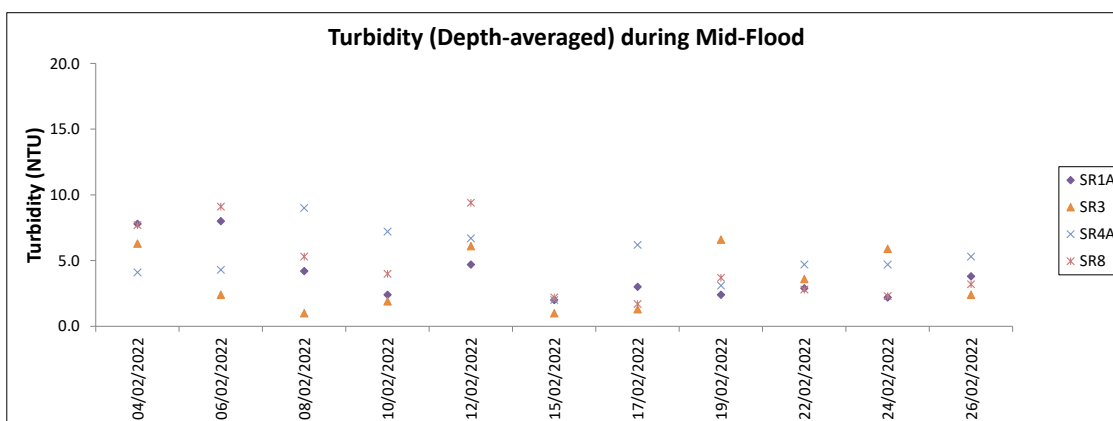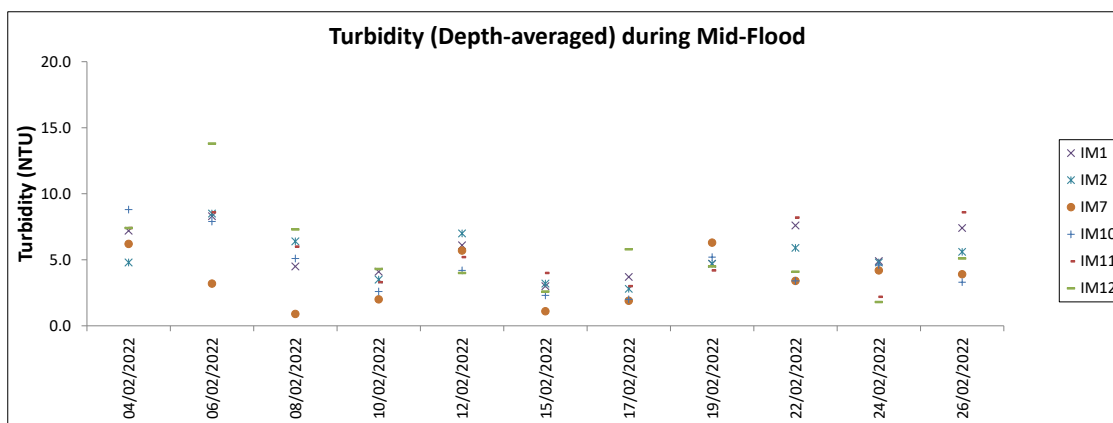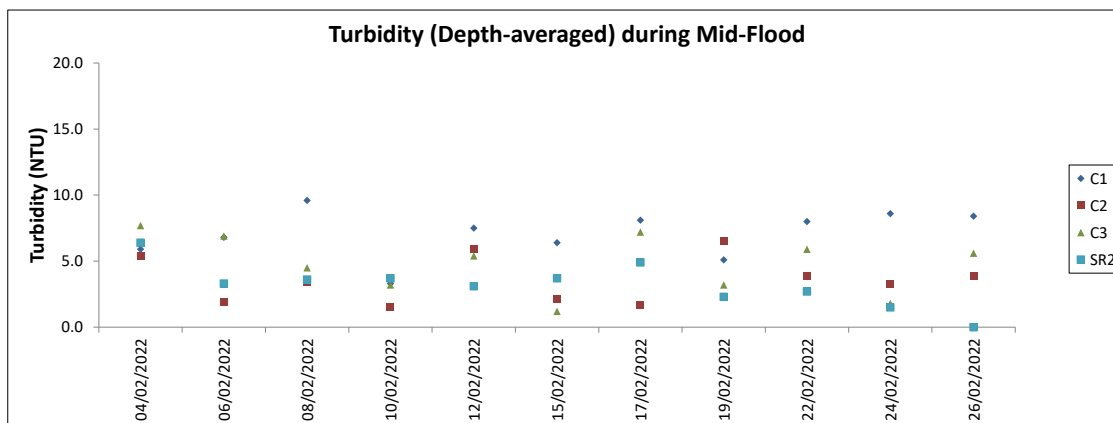



Note: The Action and Limit Level of turbidity can be referred to Table 4.2 of the monthly EM&A report.

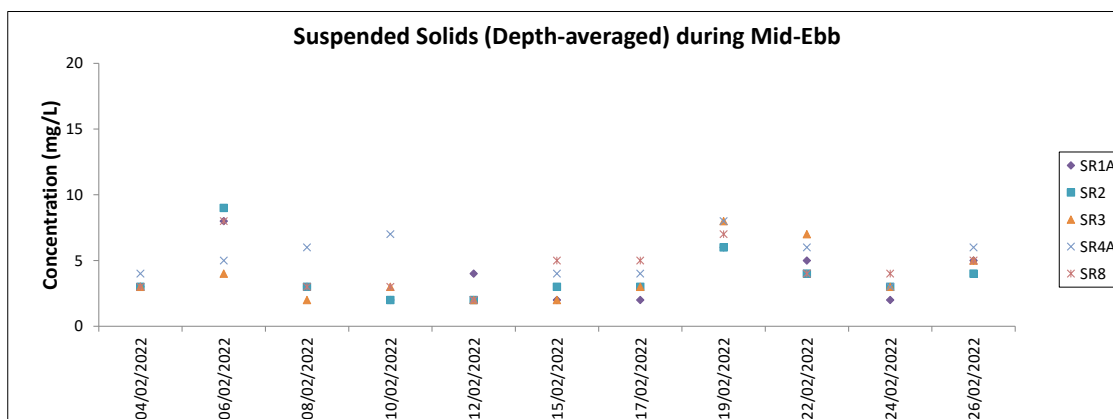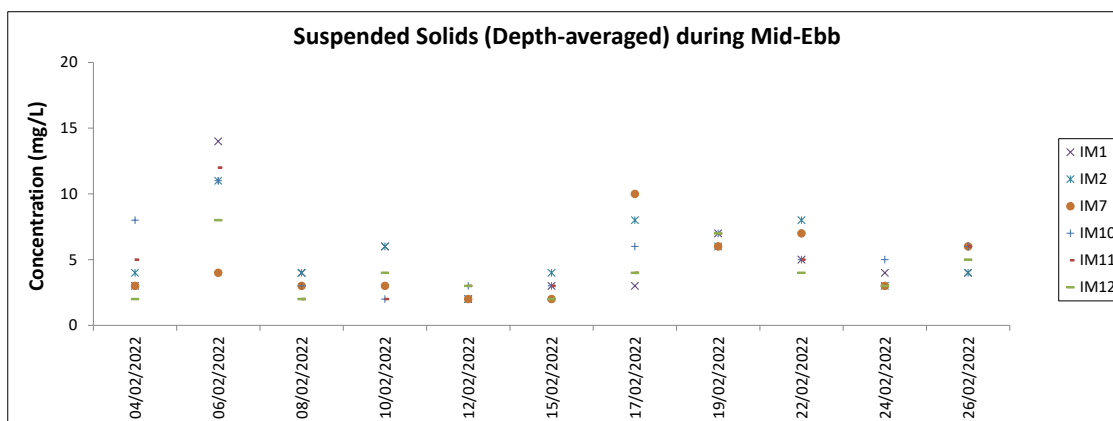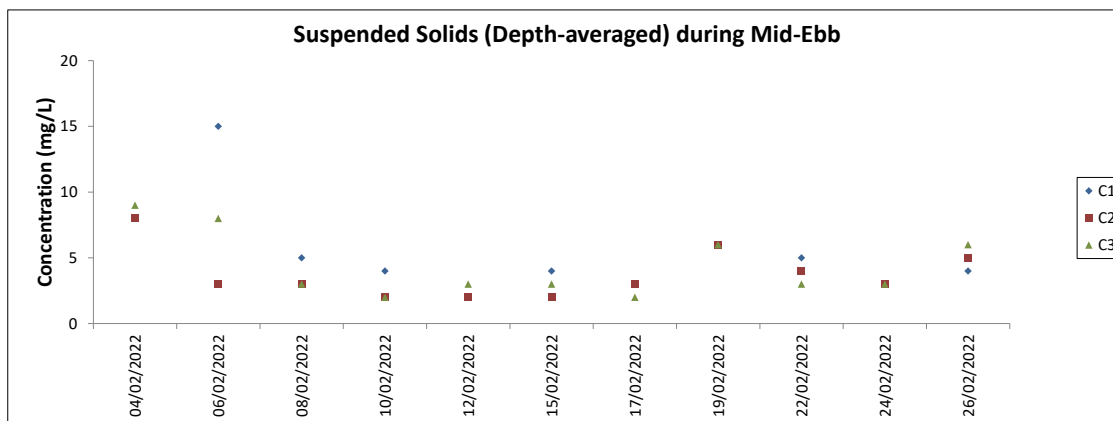



Note: The Action and Limit Level of suspended solids can be referred to Table 4.2 of the monthly EM&A report.

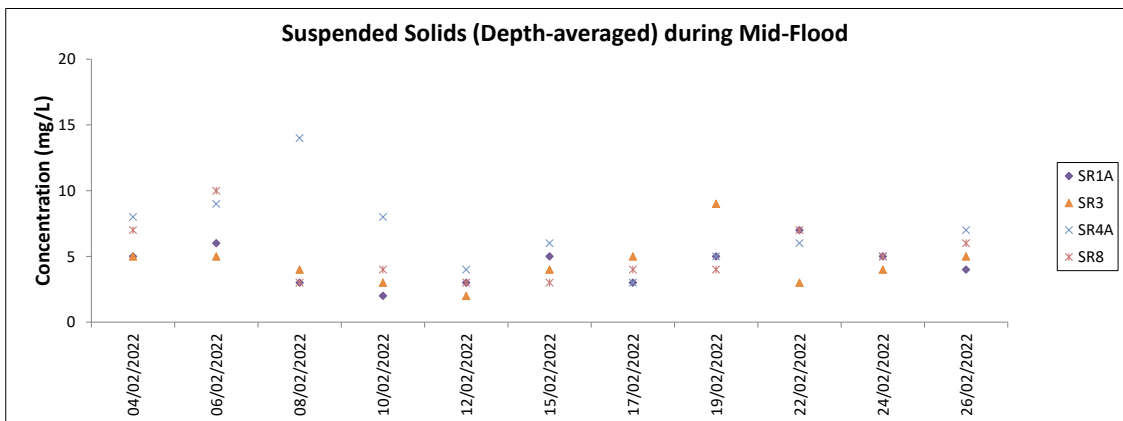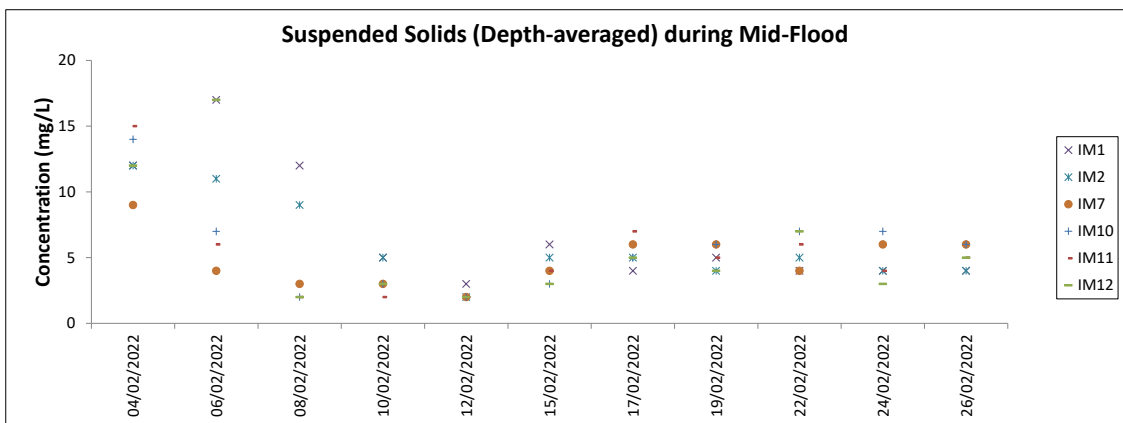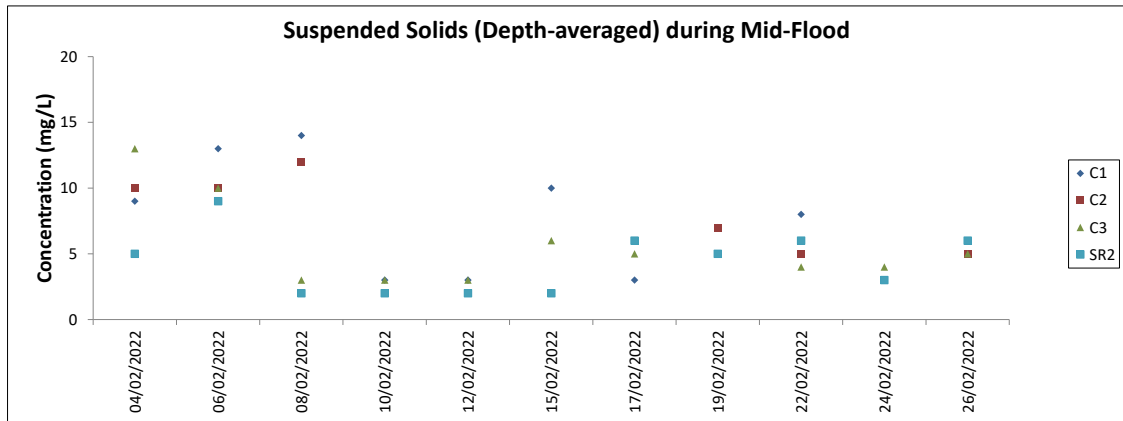



Note: The Action and Limit Level of suspended solids can be referred to Table 4.2 of the monthly EM&A report.
Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.

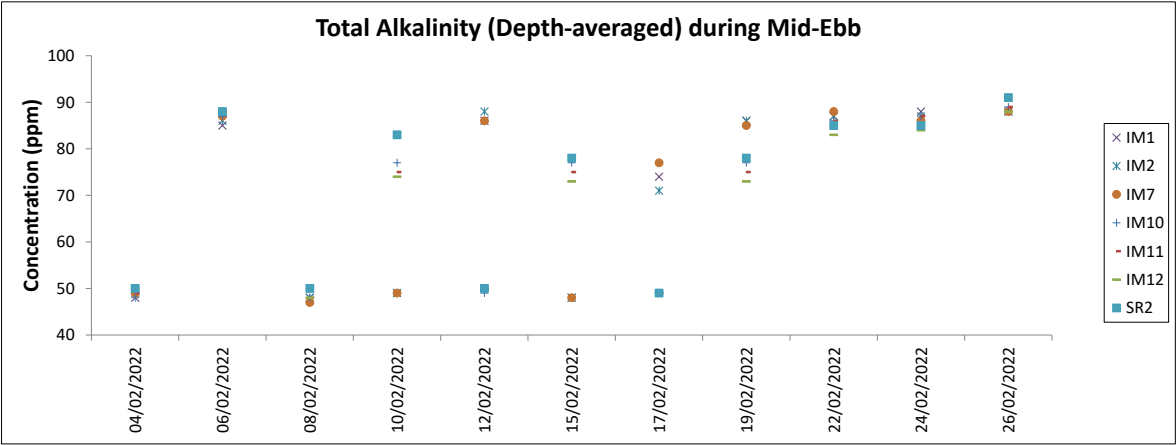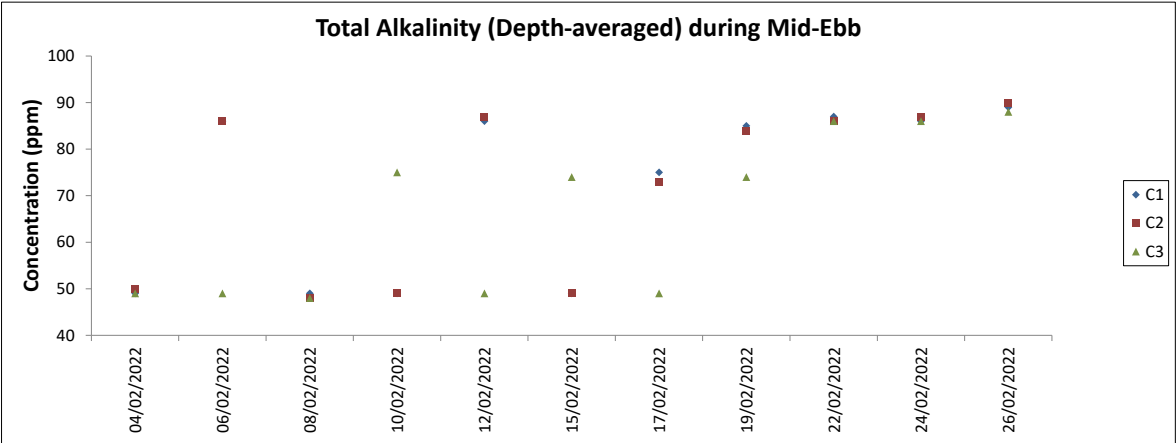



Note: The Action and Limit Level of total alkalinity can be referred to Table 4.2 of the monthly EM&A report.

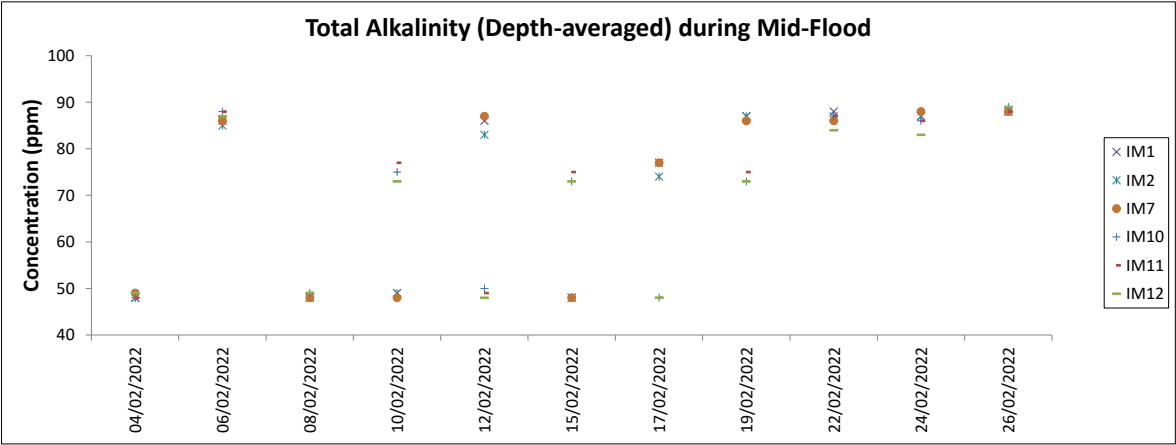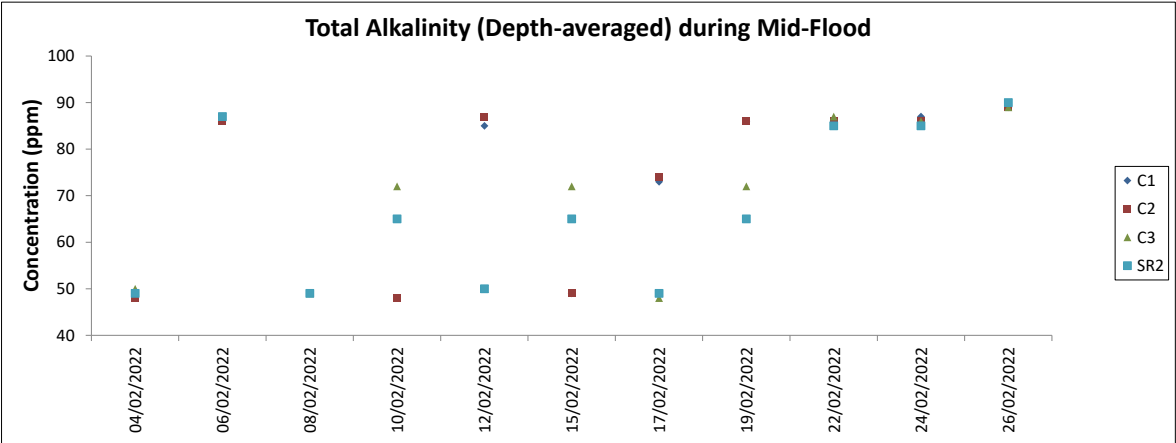



Note: The Action and Limit Level of total alkalinity can be referred to Table 4.2 of the monthly EM&A report.

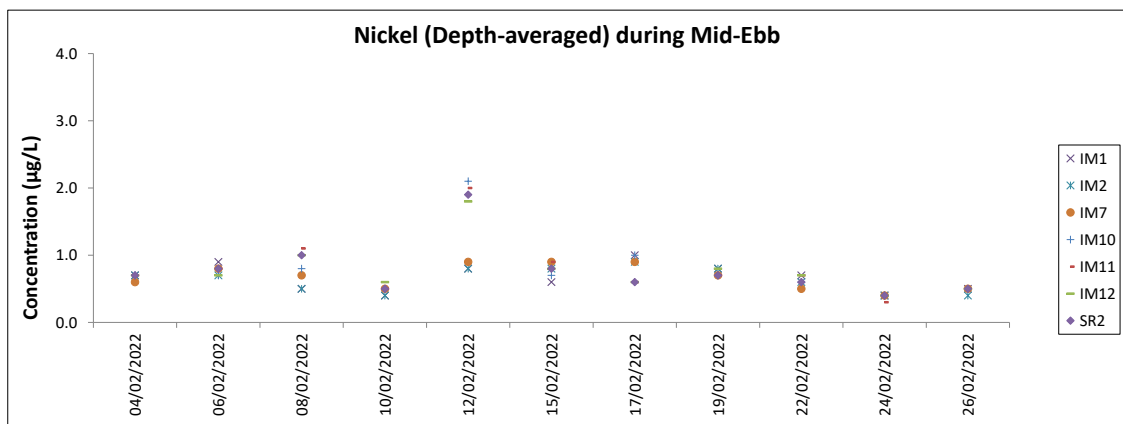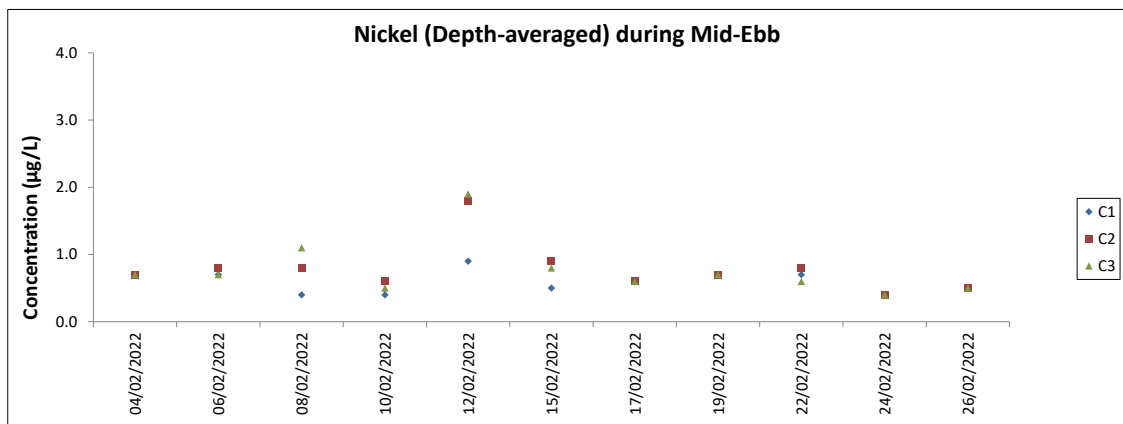

Note: The Action and Limit Level of nickel can be referred to Table 4.2 of the monthly EM&A report.

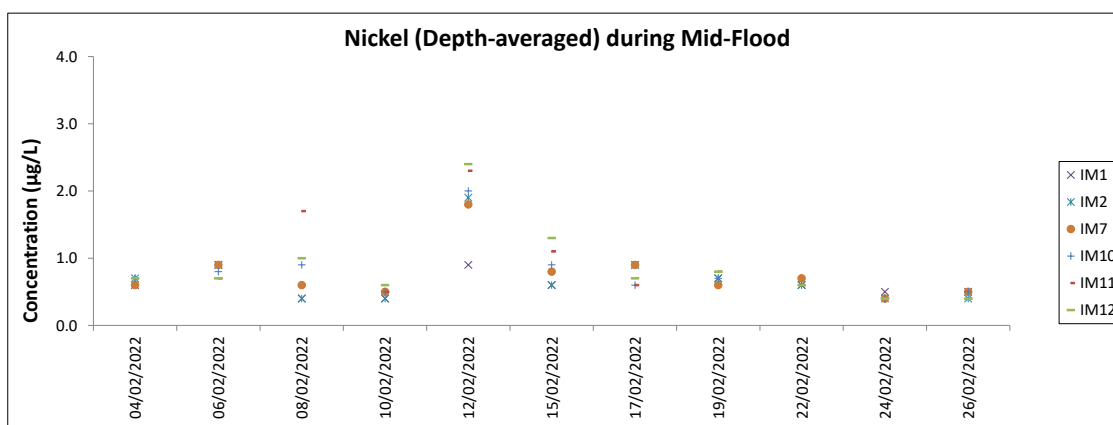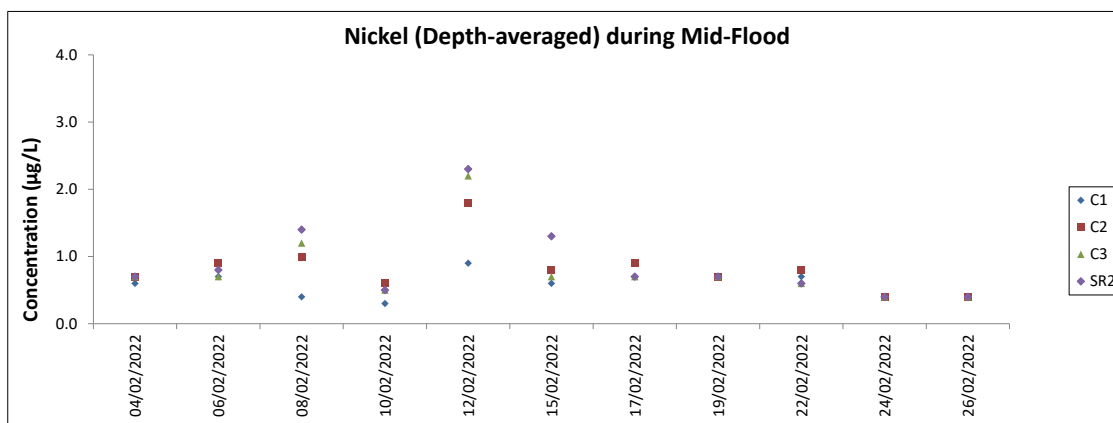

Note: The Action and Limit Level of nickel can be referred to Table 4.2 of the monthly EM&A report.
Major site activities carried out during the reporting period are summarized in Section 1.4 of the monthly EM&A report.
Weather conditions during monitoring are presented in the data tables above.
QA/ QC requirements as stipulated in the EM&A Manual were carried out during measurement.

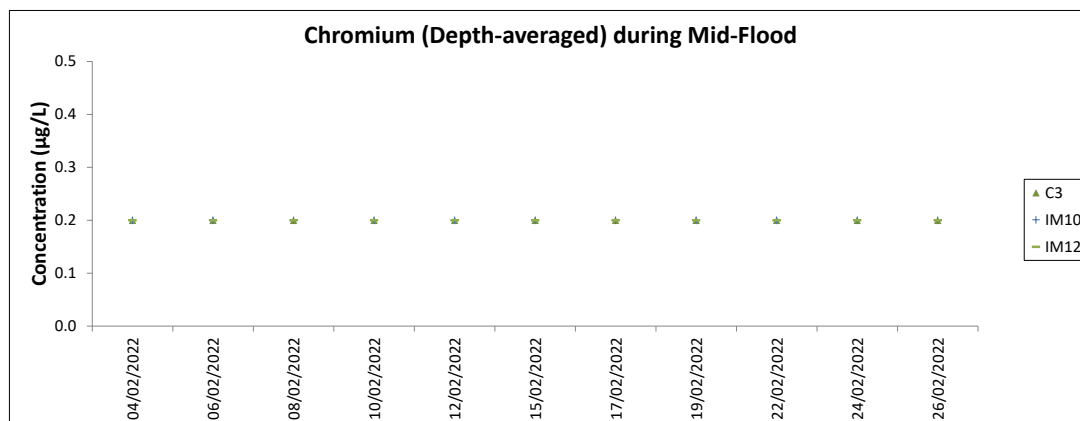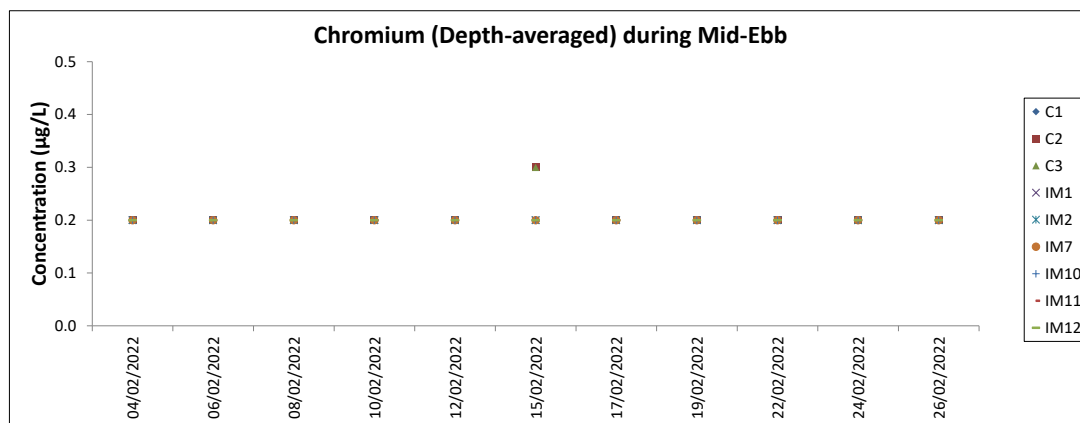

Chinese White Dolphin Monitoring Results

CWD Small Vessel Line-transect Survey

Survey Effort Data

DATE	AREA	BEAU	KM SEARCHED	SEASON	VESSEL	TYPE	P/S
1-Dec-21	NEL	3	6.110	WINTER	32166	3RS ET	P
1-Dec-21	NEL	4	30.730	WINTER	32166	3RS ET	P
1-Dec-21	NEL	3	2.210	WINTER	32166	3RS ET	P
1-Dec-21	NEL	4	7.450	WINTER	32166	3RS ET	S
3-Dec-21	NWL	3	49.900	WINTER	32166	3RS ET	P
3-Dec-21	NWL	4	14.000	WINTER	32166	3RS ET	P
3-Dec-21	NWL	3	8.400	WINTER	32166	3RS ET	S
3-Dec-21	NWL	4	3.100	WINTER	32166	3RS ET	S
6-Dec-21	SWL	2	3.350	WINTER	32166	3RS ET	P
6-Dec-21	SWL	3	50.190	WINTER	32166	3RS ET	P
6-Dec-21	SWL	2	0.900	WINTER	32166	3RS ET	S
6-Dec-21	SWL	3	14.960	WINTER	32166	3RS ET	S
7-Dec-21	NWL	2	7.900	WINTER	32166	3RS ET	P
7-Dec-21	NWL	3	53.100	WINTER	32166	3RS ET	P
7-Dec-21	NWL	4	2.000	WINTER	32166	3RS ET	S
7-Dec-21	NWL	3	12.300	WINTER	32166	3RS ET	P
13-Dec-21	NEL	2	1.290	WINTER	32166	3RS ET	P
13-Dec-21	NEL	3	29.980	WINTER	32166	3RS ET	P
13-Dec-21	NEL	4	5.880	WINTER	32166	3RS ET	P
13-Dec-21	NEL	2	0.440	WINTER	32166	3RS ET	S
13-Dec-21	NEL	3	8.270	WINTER	32166	3RS ET	S
13-Dec-21	NEL	4	1.040	WINTER	32166	3RS ET	S
15-Dec-21	AW	2	4.940	WINTER	32166	3RS ET	P
15-Dec-21	WL	2	19.188	WINTER	32166	3RS ET	P
15-Dec-21	WL	2	10.482	WINTER	32166	3RS ET	S
16-Dec-21	SWL	2	28.760	WINTER	32166	3RS ET	P
16-Dec-21	SWL	3	26.150	WINTER	32166	3RS ET	P
16-Dec-21	SWL	2	6.185	WINTER	32166	3RS ET	S
16-Dec-21	SWL	3	8.280	WINTER	32166	3RS ET	S
17-Dec-21	AW	3	4.970	WINTER	32166	3RS ET	P
17-Dec-21	WL	3	11.890	WINTER	32166	3RS ET	P
17-Dec-21	WL	4	8.700	WINTER	32166	3RS ET	P
17-Dec-21	WL	3	6.710	WINTER	32166	3RS ET	S
17-Dec-21	WL	4	4.000	WINTER	32166	3RS ET	S
03-Jan-22	NWL	2	48.340	WINTER	32166	3RS ET	P
03-Jan-22	NWL	3	13.940	WINTER	32166	3RS ET	P
03-Jan-22	NWL	2	11.440	WINTER	32166	3RS ET	S
04-Jan-22	NEL	2	6.300	WINTER	32166	3RS ET	P
04-Jan-22	NEL	3	23.630	WINTER	32166	3RS ET	P
04-Jan-22	NEL	4	7.300	WINTER	32166	3RS ET	P
04-Jan-22	NEL	3	7.770	WINTER	32166	3RS ET	S
04-Jan-22	NEL	4	1.800	WINTER	32166	3RS ET	S
05-Jan-22	AW	2	0.800	WINTER	32166	3RS ET	P
05-Jan-22	AW	3	1.770	WINTER	32166	3RS ET	P
05-Jan-22	AW	4	1.920	WINTER	32166	3RS ET	P
05-Jan-22	WL	2	10.474	WINTER	32166	3RS ET	P
05-Jan-22	WL	2	5.590	WINTER	32166	3RS ET	S

DATE	AREA	BEAU	KM SEARCHED	SEASON	VESSEL	TYPE	P/S
05-Jan-22	WL	3	0.504	WINTER	32166	3RS ET	S
10-Jan-22	AW	2	4.820	WINTER	32166	3RS ET	P
10-Jan-22	WL	2	12.835	WINTER	32166	3RS ET	P
10-Jan-22	WL	3	6.493	WINTER	32166	3RS ET	P
10-Jan-22	WL	2	5.225	WINTER	32166	3RS ET	S
10-Jan-22	WL	3	4.587	WINTER	32166	3RS ET	S
11-Jan-22	NEL	2	7.450	WINTER	32166	3RS ET	P
11-Jan-22	NEL	3	28.850	WINTER	32166	3RS ET	P
11-Jan-22	NEL	4	1.100	WINTER	32166	3RS ET	P
11-Jan-22	NEL	2	3.390	WINTER	32166	3RS ET	S
11-Jan-22	NEL	3	5.510	WINTER	32166	3RS ET	S
11-Jan-22	NEL	4	0.800	WINTER	32166	3RS ET	S
12-Jan-22	NWL	2	12.600	WINTER	32166	3RS ET	P
12-Jan-22	NWL	3	50.400	WINTER	32166	3RS ET	P
12-Jan-22	NWL	2	3.300	WINTER	32166	3RS ET	S
12-Jan-22	NWL	3	8.600	WINTER	32166	3RS ET	S
13-Jan-22	SWL	2	38.742	WINTER	32166	3RS ET	P
13-Jan-22	SWL	3	14.940	WINTER	32166	3RS ET	P
13-Jan-22	SWL	2	13.268	WINTER	32166	3RS ET	S
13-Jan-22	SWL	3	2.260	WINTER	32166	3RS ET	S
19-Jan-22	SWL	2	26.240	WINTER	32166	3RS ET	P
19-Jan-22	SWL	3	21.930	WINTER	32166	3RS ET	P
19-Jan-22	SWL	4	5.500	WINTER	32166	3RS ET	P
19-Jan-22	SWL	2	10.780	WINTER	32166	3RS ET	S
19-Jan-22	SWL	3	3.510	WINTER	32166	3RS ET	S
19-Jan-22	SWL	4	1.920	WINTER	32166	3RS ET	S
7-Feb-22	NEL	2	22.800	WINTER	32166	3RS ET	P
7-Feb-22	NEL	3	7.990	WINTER	32166	3RS ET	P
7-Feb-22	NEL	4	5.840	WINTER	32166	3RS ET	P
7-Feb-22	NEL	2	7.900	WINTER	32166	3RS ET	S
7-Feb-22	NEL	3	1.000	WINTER	32166	3RS ET	S
7-Feb-22	NEL	4	1.070	WINTER	32166	3RS ET	S
8-Feb-22	AW	3	4.930	WINTER	32166	3RS ET	P
8-Feb-22	WL	3	14.850	WINTER	32166	3RS ET	P
8-Feb-22	WL	4	5.800	WINTER	32166	3RS ET	P
8-Feb-22	WL	2	1.220	WINTER	32166	3RS ET	S
8-Feb-22	WL	3	7.030	WINTER	32166	3RS ET	S
8-Feb-22	WL	4	2.000	WINTER	32166	3RS ET	S
9-Feb-22	NWL	3	47.720	WINTER	32166	3RS ET	P
9-Feb-22	NWL	4	16.480	WINTER	32166	3RS ET	P
9-Feb-22	NWL	3	11.700	WINTER	32166	3RS ET	S
10-Feb-22	AW	2	4.770	WINTER	32166	3RS ET	P
10-Feb-22	WL	3	19.968	WINTER	32166	3RS ET	P
10-Feb-22	WL	3	9.014	WINTER	32166	3RS ET	S
14-Feb-22	NEL	2	33.240	WINTER	32166	3RS ET	P
14-Feb-22	NEL	3	3.440	WINTER	32166	3RS ET	P
14-Feb-22	NEL	2	9.120	WINTER	32166	3RS ET	S
14-Feb-22	NEL	3	1.200	WINTER	32166	3RS ET	S
15-Feb-22	NWL	2	48.350	WINTER	32166	3RS ET	P

DATE	AREA	BEAU	KM SEARCHED	SEASON	VESSEL	TYPE	P/S
15-Feb-22	NWL	3	14.780	WINTER	32166	3RS ET	P
15-Feb-22	NWL	2	7.770	WINTER	32166	3RS ET	S
15-Feb-22	NWL	3	3.400	WINTER	32166	3RS ET	S
2-Mar-22	SWL	1	19.328	WINTER	32166	3RS ET	P
2-Mar-22	SWL	2	26.443	WINTER	32166	3RS ET	P
2-Mar-22	SWL	3	4.330	WINTER	32166	3RS ET	P
2-Mar-22	SWL	1	5.230	WINTER	32166	3RS ET	S
2-Mar-22	SWL	2	10.819	WINTER	32166	3RS ET	S
2-Mar-22	SWL	3	1.616	WINTER	32166	3RS ET	S
4-Mar-22	SWL	1	3.665	WINTER	32166	3RS ET	P
4-Mar-22	SWL	2	12.934	WINTER	32166	3RS ET	P
4-Mar-22	SWL	3	31.502	WINTER	32166	3RS ET	P
4-Mar-22	SWL	2	3.628	WINTER	32166	3RS ET	S
4-Mar-22	SWL	3	11.733	WINTER	32166	3RS ET	S

Notes: CWD monitoring survey data of the two preceding survey months are presented for reference only. The two vessel surveys of February in SWL survey area were rescheduled to early March (i.e., 2 and 4 March 2022) due to unavailability of vessel operators or suitable vessel during the rising impact of COVID-19 pandemic in the second half of February 2022.

CWD Small Vessel Line-transect Survey

Sighting Data

DATE	STG #	TIME	CWD/FP	GP SZ	AREA	BEAU	PSD	EFFORT	TYPE	DEC LAT	DEC LON	SEASON	BOAT ASSOC.	P/S
6-Dec-21	1	1119	FP	1	SWL	3	11	ON	3RS ET	22.1765	113.9280	WINTER	NONE	P
6-Dec-21	2	1504	CWD	3	SWL	3	22	ON	3RS ET	22.1878	113.8497	WINTER	NONE	P
7-Dec-21	1	0945	CWD	1	NWL	2	N/A	OFF	3RS ET	22.3983	113.8873	WINTER	NONE	N/A
15-Dec-21	1	1043	CWD	4	WL	2	471	ON	3RS ET	22.2500	113.8357	WINTER	NONE	P
15-Dec-21	2	1112	CWD	1	WL	2	113	ON	3RS ET	22.2415	113.8315	WINTER	NONE	P
16-Dec-21	1	1333	CWD	5	SWL	2	134	ON	3RS ET	22.1885	113.8880	WINTER	NONE	P
16-Dec-21	2	1448	CWD	1	SWL	2	16	ON	3RS ET	22.1989	113.8685	WINTER	NONE	P
16-Dec-21	3	1507	CWD	3	SWL	2	63	ON	3RS ET	22.1998	113.8622	WINTER	GILLNETTER	S
03-Jan-22	1	0959	CWD	3	NWL	3	868	ON	3RS ET	22.3497	113.8684	WINTER	NONE	P
03-Jan-22	2	1039	CWD	5	NWL	2	466	ON	3RS ET	22.2726	113.8700	WINTER	GILLNETTER	P
03-Jan-22	3	1159	CWD	4	NWL	2	130	ON	3RS ET	22.3693	113.8773	WINTER	NONE	P
03-Jan-22	4	1331	CWD	2	NWL	2	563	ON	3RS ET	22.3616	113.8979	WINTER	NONE	P
05-Jan-22	1	0946	CWD	1	AW	3	262	ON	3RS ET	22.2919	113.8752	WINTER	NONE	P
05-Jan-22	2	1024	CWD	5	WL	2	430	ON	3RS ET	22.2854	113.8614	WINTER	GILLNETTER	P
05-Jan-22	3	1048	CWD	3	WL	2	789	ON	3RS ET	22.2764	113.8512	WINTER	NONE	S
05-Jan-22	4	1052	CWD	3	WL	2	173	ON	3RS ET	22.2749	113.8492	WINTER	NONE	S
05-Jan-22	5	1108	CWD	3	WL	2	295	ON	3RS ET	22.2695	113.8523	WINTER	GILLNETTER	P
05-Jan-22	6	1115	CWD	1	WL	2	8	ON	3RS ET	22.2683	113.8597	WINTER	GILLNETTER	S
05-Jan-22	7	1125	CWD	7	WL	2	178	ON	3RS ET	22.2593	113.8440	WINTER	NONE	P
05-Jan-22	8	1143	CWD	3	WL	2	155	ON	3RS ET	22.2502	113.8373	WINTER	NONE	P
05-Jan-22	9	1159	CWD	1	WL	2	304	ON	3RS ET	22.2448	113.8497	WINTER	GILLNETTER	S
05-Jan-22	10	1233	CWD	4	WL	2	74	ON	3RS ET	22.2323	113.8373	WINTER	NONE	P
05-Jan-22	11	1253	CWD	3	WL	2	215	ON	3RS ET	22.2236	113.8309	WINTER	NONE	P
05-Jan-22	12	1313	CWD	1	WL	2	240	ON	3RS ET	22.2142	113.8264	WINTER	NONE	P
05-Jan-22	13	1328	CWD	11	WL	2	598	ON	3RS ET	22.2060	113.8393	WINTER	NONE	S
10-Jan-22	1	1017	CWD	1	WL	2	63	ON	3RS ET	22.2759	113.8501	WINTER	NONE	S
10-Jan-22	2	1140	CWD	5	WL	3	331	ON	3RS ET	22.2142	113.8259	WINTER	NONE	P
10-Jan-22	3	1211	CWD	8	WL	3	103	ON	3RS ET	22.2059	113.8291	WINTER	NONE	P
13-Jan-22	1	1152	FP	1	SWL	2	40	ON	3RS ET	22.1586	113.9179	WINTER	NONE	P
13-Jan-22	2	1314	FP	3	SWL	2	261	ON	3RS ET	22.1492	113.8923	WINTER	NONE	S
13-Jan-22	3	1433	CWD	5	SWL	2	366	ON	3RS ET	22.1978	113.8685	WINTER	NONE	P
19-Jan-22	1	1337	FP	2	SWL	3	43	ON	3RS ET	22.1859	113.8977	WINTER	NONE	P

DATE	STG #	TIME	CWD/FP	GP SZ	AREA	BEAU	PSD	EFFORT	TYPE	DEC LAT	DEC LON	SEASON	BOAT ASSOC.	P/S
19-Jan-22	2	1453	CWD	5	SWL	3	38	ON	3RS ET	22.1827	113.8592	WINTER	NONE	P
10-Feb-22	1	1102	CWD	9	WL	3	185	ON	3RS ET	22.2418	113.8301	WINTER	NONE	P
10-Feb-22	2	1119	CWD	1	WL	3	61	ON	3RS ET	22.2316	113.8319	WINTER	NONE	P
10-Feb-22	3	1134	CWD	4	WL	3	78	ON	3RS ET	22.2236	113.8286	WINTER	NONE	P
10-Feb-22	4	1157	CWD	2	WL	3	43	ON	3RS ET	22.2146	113.8308	WINTER	NONE	P
15-Feb-22	1	0950	CWD	3	NWL	2	97	ON	3RS ET	22.3634	113.8706	WINTER	NONE	P
15-Feb-22	2	1054	CWD	2	NWL	2	50	ON	3RS ET	22.3039	113.8778	WINTER	NONE	P
2-Mar-22	1	1023	FP	6	SWL	1	400	ON	3RS ET	22.2167	113.9352	WINTER	NONE	P
2-Mar-22	2	1034	FP	3	SWL	1	88	ON	3RS ET	22.1947	113.9360	WINTER	NONE	P
2-Mar-22	3	1040	FP	2	SWL	1	50	ON	3RS ET	22.1843	113.9360	WINTER	NONE	P
2-Mar-22	4	1112	FP	3	SWL	1	474	ON	3RS ET	22.1693	113.9277	WINTER	NONE	P
2-Mar-22	5	1132	FP	5	SWL	1	44	ON	3RS ET	22.2034	113.9187	WINTER	NONE	S
2-Mar-22	6	1154	FP	1	SWL	2	80	ON	3RS ET	22.1584	113.9175	WINTER	NONE	P
2-Mar-22	7	1204	FP	1	SWL	2	20	ON	3RS ET	22.1413	113.9154	WINTER	NONE	S
2-Mar-22	8	1213	FP	2	SWL	2	62	ON	3RS ET	22.1522	113.9082	WINTER	NONE	P
2-Mar-22	9	1217	FP	2	SWL	2	6	ON	3RS ET	22.1543	113.9050	WINTER	NONE	S
2-Mar-22	10	1310	FP	4	SWL	1	152	ON	3RS ET	22.1701	113.8969	WINTER	NONE	P
2-Mar-22	11	1316	FP	3	SWL	2	306	ON	3RS ET	22.1590	113.8973	WINTER	NONE	P
2-Mar-22	12	1318	FP	6	SWL	2	61	ON	3RS ET	22.1573	113.8974	WINTER	NONE	P
2-Mar-22	13	1328	FP	2	SWL	2	39	ON	3RS ET	22.1495	113.8906	WINTER	NONE	S
2-Mar-22	14	1335	FP	7	SWL	2	69	ON	3RS ET	22.1588	113.8882	WINTER	NONE	P
2-Mar-22	15	1346	FP	1	SWL	1	43	ON	3RS ET	22.1646	113.8883	WINTER	NONE	P
2-Mar-22	16	1427	FP	1	SWL	2	453	ON	3RS ET	22.1757	113.8791	WINTER	NONE	P
2-Mar-22	17	1429	FP	1	SWL	2	10	ON	3RS ET	22.1729	113.8786	WINTER	NONE	P
2-Mar-22	18	1434	FP	4	SWL	2	34	ON	3RS ET	22.1668	113.8789	WINTER	NONE	P
4-Mar-22	1	1025	FP	2	SWL	1	156	ON	3RS ET	22.2173	113.9361	WINTER	NONE	P
4-Mar-22	2	1028	FP	5	SWL	1	45	ON	3RS ET	22.2140	113.9361	WINTER	NONE	P
4-Mar-22	3	1035	FP	1	SWL	1	11	ON	3RS ET	22.2073	113.9362	WINTER	NONE	P
4-Mar-22	4	1042	FP	2	SWL	2	264	ON	3RS ET	22.1863	113.9362	WINTER	NONE	P
4-Mar-22	5	1215	FP	5	SWL	3	6	ON	3RS ET	22.1522	113.9075	WINTER	NONE	P
4-Mar-22	6	1229	FP	4	SWL	3	104	ON	3RS ET	22.1561	113.8999	WINTER	NONE	S
4-Mar-22	7	1329	FP	1	SWL	3	21	ON	3RS ET	22.1568	113.8976	WINTER	NONE	P
4-Mar-22	8	1405	FP	1	SWL	2	73	ON	3RS ET	22.2085	113.8882	WINTER	NONE	P

DATE	STG #	TIME	CWD/FP	GP SZ	AREA	BEAU	PSD	EFFORT	TYPE	DEC LAT	DEC LON	SEASON	BOAT ASSOC.	P/S
4-Mar-22	9	1411	FP	3	SWL	2	80	ON	3RS ET	22.2114	113.8837	WINTER	NONE	S
4-Mar-22	10	1415	FP	2	SWL	2	102	ON	3RS ET	22.2081	113.8794	WINTER	NONE	S
4-Mar-22	11	1530	CWD	1	SWL	2	262	ON	3RS ET	22.1899	113.8495	WINTER	NONE	P

Abbreviations: STG# = Sighting Number; GP SZ = Group Size; BEAU = Beaufort Sea State; PSD = Perpendicular Distance (in metres); N/A = Not Applicable; DEC LAT = Latitude (WGS84 in Decimal), DEC LON = Longitude (WGS84 in Decimal); BOAT ASSOC. = Fishing Boat Association; P/S = Primary Transect / Secondary Transect

Notes:

The two vessel surveys of February in SWL survey area were rescheduled to early March (i.e., 2 and 4 March 2022) due to unavailability of vessel operators or suitable vessel during the rising impact of COVID-19 pandemic in the second half of February 2022.

CWD monitoring survey data of the two preceding survey months are presented for reference only. No relevant figure or text will be mentioned in this monthly EM&A report.

Sighting data of finless porpoise (FP) are presented for reference only. No relevant figure or text will be mentioned in the monthly EM&A report. All FP sightings are excluded in calculation.

Calculation of the encounter rates STG and ANI in the whole survey area (NEL, NWL, AW, WL, SWL):

A total of 413.420 km of survey effort was collected under Beaufort Sea State 3 or below with favourable visibility; total no. of 7 on-effort sightings and total number of 22 dolphins from on-effort sightings were collected under such condition. Calculation of the encounter rates in February 2022 are shown as below:

Encounter Rate by Number of Dolphin Sightings (STG) in February 2022

$$STG = \frac{7}{413.420} \times 100 = 1.69$$

Encounter Rate by Number of Dolphins (ANI) in February 2022

$$ANI = \frac{22}{413.420} \times 100 = 5.32$$

Calculation of the running quarterly STG and ANI in the whole survey area (NEL, NWL, AW, WL, SWL):

A total of 1206.563 km of survey effort was collected under Beaufort Sea State 3 or below with favourable visibility; total no. of 35 on-effort sightings and total number of 123 dolphins from on-effort sightings were collected under such condition. Calculation of the running quarterly encounter rates are shown as below:

Running Quarterly Encounter Rate by Number of Dolphin Sightings (STG)

$$STG = \frac{35}{1206.563} \times 100 = 2.90$$

Running Quarterly Encounter Rate by Number of Dolphins (ANI)

$$ANI = \frac{123}{1206.563} \times 100 = 10.19$$

CWD Small Vessel Line-transect Survey

Photo Identification

	
SLMM007_20220210_1_1	SLMM073_20220210_1_2
	
WLMM028_20220210_1_5	WLMM109_20220210_1_3
	
WLMM114_20220210_1_2	WLMM152_20220210_1_1
	
NLMM013_20220215_1_8	NLMM028_20220215_1_9

	
WLMM019_20220215_1_1	

CWD Land-based Theodolite Tracking Survey**CWD Groups by Survey Date**

Date	Station	Start Time	End Time	Duration	Beaufort Range	Visibility	No. of Focal Follow Dolphin Groups Tracked	Dolphin Group Size Range
11/Feb/22	Lung Kwu Chau	8:51	14:51	6:00	2	3-4	1	1
16/Feb/22	Sha Chau	10:35	16:35	6:00	2-4	2	0	0

Visibility: 1=Excellent, 2=Good, 3=Fair, 4=Poor

Appendix D. Status of Environmental Permits and Licenses

Description		Permit/ Reference No.	Status
EIAO	Environmental Permit	EP-489/2014	Approved on 7 Nov 2014

Contract No.	Description	Location	Permit/ Reference No.	Status
3206	Notification of Construction Work under APCO	Works area of 3206	409237	Receipt acknowledged by EPD on 25 Oct 2016
	Registration as Chemical Waste Producer	Site office of 3206	WPN 5213-951-Z4035-01	Completion of Registration on 18 Nov 2016
		Works area of 3206	WPN 5213-951-Z4035-02	Completion of Registration on 18 Nov 2016
	Construction Noise Permit (General Works)	Works Area of 3206	GW-RS0757-21	Valid from 6 Oct 2021 to 2 Apr 2022
	Bill Account for disposal	Works area of 3206	A/C 7026398	Approval granted from EPD on 16 Nov 2016
3301	Notification of Construction Work under APCO	Works area of 3301	415821	Receipt acknowledged by EPD on 19 Apr 2017
	Registration as Chemical Waste Producer	Works area of 3301	WPN 5213-951-F2718-02	Completion of Registration on 9 Jun 2017
	Discharge License under WPCO	Works area of 3301	WT00029286-2017	Valid from 20 Sep 2017 to 30 Sep 2022
	Bill Account for disposal	Works area of 3301	A/C 7027728	Approval granted from EPD on 8 May 2017
	Construction Noise Permit (General Works)	Works area of 3301	GW-RS0631-21	Valid from 22 Aug 2021 to 21 Feb 2022
		Works area of 3301 (Cable ducting works) (Special Case)	GW-RS0744-21	Valid from 2 Oct 2021 to 29 Mar 2022
3302	Notification of Construction Work under APCO	Works area of 3302	440222	Receipt acknowledged by EPD on 10 Dec 2018
		Staging area of 3302	2018CES1	Receipt acknowledged by EPD on 21 Dec 2018
			454882	Receipt acknowledged by EPD on 2 Apr 2020
			476068	Receipt acknowledged by EPD on 17 Jan 2022

Contract No.	Description	Location	Permit/ Reference No.	Status
	Registration as Chemical Waste Producer	Works area of 3302	5296-951-C4331-01	Completion of Registration on 4 Jan 2019
	Discharge License under WPCO	Works area of 3302	WT00034539-2019	Valid from 11 Mar 2020 to 31 Mar 2025
		Works area of 3302	WT00034541-2019	Valid from 14 Oct 2019 to 31 Oct 2024
	Bill Account for disposal	Works area of 3302	A/C 7032881	Approval granted from EPD on 8 Jan 2019
	Construction Noise Permit (General Works)	Works area of 3302	GW-RS0842-21	Valid from 10 Nov 2021 to 8 May 2022
			GW-RS1005-21	Valid from 7 Jan 2022 to 6 Jul 2022
3303	Notification of Construction Work under APCO	Works area of 3303	445611	Receipt acknowledged by EPD on 27 May 2019
	Specified Process license under APCO	Works area of 3303	L-15-040 (1)	Valid from 29 Mar 2021 to 28 Mar 2025
	Registration as Chemical Waste Producer	Works area of 3303	5213-951-S4174-01	Completion of Registration on 17 Jun 2019
	Discharge License under WPCO	Works area of 3303	WT00035689-2020	Valid from 11 May 2020 to 31 May 2025
		Works area of 3303	WT00036734-2020	Valid from 1 Dec 2020 to 31 Dec 2025
	Bill Account for disposal	Works area of 3303	A/C 7034272	Approval granted from EPD on 10 Jun 2019
	Construction Noise Permit (General Works)	Works area of 3303 (Existing airport)	GW-RS0823-21	Valid from 16 Nov 2021 to 15 May 2022
		Works area of 3303 (Reclamation area)	GW-RS0803-21	Superseded by GW-RS0066-22
3305		Works area of 3303 (Reclamation area)	GW-RS0066-22	Valid from 31 Jan 2022 to 30 Jul 2022
	Notification of Construction Work under APCO	Works area of 3305	460857	Receipt acknowledged by EPD on 12 Oct 2020
	Registration as Chemical Waste Producer	Works area of 3305	5213-951-A3024-01	Completion of Registration on 13 Nov 2020
3306	Bill Account for disposal	Works area of 3305	A/C 7035360	Approval granted from EPD on 9 Oct 2019
	Registration as Chemical Waste Producer	Works area of 3306	8335-951-C4434-01	Completion of Registration on 1 Apr 2020
3307	Bill Account for disposal	Works area of 3306	A/C 7035868	Approval granted from EPD on 27 Nov 2019
	Notification of Construction Work under APCO	Works area of 3307	454964	Receipt acknowledged by EPD on 6 Apr 2020
	Registration as Chemical Waste Producer	Works area of 3307	5211-951-P3379-01	Completion of Registration on 8 Jun 2020

Contract No.	Description	Location	Permit/ Reference No.	Status
	Discharge License under WPCO	Works area of 3307	WT00036926-2020	Valid from 31 Dec 2020 to 31 Dec 2025
	Bill Account for disposal	Works area of 3307	A/C 7037129	Approval granted from EPD on 5 May 2020
	Construction Noise Permit (General Works)	Works area of 3307	GW-RS0562-21	Valid from 6 Aug 2021 to 5 Feb 2022
		Works area of 3307	GW-RS0052-22	Valid from 6 Feb 2022 to 5 Aug 2022
3308	Bill Account for disposal	Works area of 3308	A/C 7038988	Approval granted from EPD on 24 Nov 2020
	Construction Noise Permit (General Works)	Works area of 3308	GW-RS0655-21	Valid from 2 Sep 2021 to 28 Feb 2022
3310	Notification of Construction Work under APCO	Works area of 3310	474782	Receipt acknowledged by EPD on 10 Dec 2021
	Registration as Chemical Waste Producer	Works area of 3310	5213-951-C4682-01	Completion of Registration on 21 Dec 2021
	Discharge License under WPCO	Works area of 3310	WT00039654-2021	Valid from 31 Dec 2021 to 31 Dec 2026
	Bill Account for disposal	Works area of 3310	A/C 7042793	Approval granted from EPD on 4 Jan 2022
	Construction Noise Permit (General Works)	Works area of 3310	GW-RS1038-21	Valid from 28 Dec 2021 to 27 Jun 2022
3402	Bill Account for disposal	Works area of 3402	A/C 7032577	Approval granted from EPD on 27 Nov 2018
3403	Notification of Construction Work under APCO	Works area of 3403	450860	Receipt acknowledged by EPD on 11 Nov 2019
		Works area of 3403 (with Area 17 and Area 15)	475369	Receipt acknowledged by EPD on 28 Dec 2021
	Registration as Chemical Waste Producer	Works area of 3403	WPN 5213-951-S4218-01	Completion of Registration on 9 Jan 2020
	Discharge License under WPCO	Works area of 3403	WT00035841-2020	Valid from 5 Jun 2020 to 30 Jun 2025
	Bill Account for disposal	Works area of 3403	A/C 7035267	Approval granted from EPD on 30 Sep 2019
	Construction Noise Permit (General Works)	Works area of 3403	GW-RS0653-21	Valid from 4 Sep 2021 to 28 Feb 2022
	Construction Noise Permit (Special Case)	Works area of 3403	GW-RS0909-21	Valid from 1 Dec 2021 to 31 May 2022
3404	Bill Account for disposal	Works area of 3404	A/C 7035158	Approval granted from EPD on 12 Sep 2019
3405	Notification of Construction Work under APCO	Works area of 3405	453447	Receipt acknowledged by EPD on 18 Feb 2020
	Registration as Chemical Waste Producer	Works area of 3405	WPN 5218-951-C4431-01	Completion of Registration on 12 Mar 2020

Contract No.	Description	Location	Permit/ Reference No.	Status
	Discharge License under WPCO	Works area of 3405	WT00037084-2020	Valid from 17 Mar 2021 to 31 Mar 2026
	Bill Account for disposal	Works area of 3405	A/C 7036796	Approval granted from EPD on 20 Mar 2020
	Construction Noise Permit (General Works)	Works area of 3405	GW-RS0966-21	Valid from 13 Dec 2021 to 12 Jun 2022
3408	Notification of Construction Work under APCO	Works area of 3408	461958	Receipt acknowledged by EPD on 17 Nov 2020
	Registration as Chemical Waste Producer	Works area of 3408	WPN 5218-951-B2621-01	Completion of Registration on 16 Jul 2021
	Discharge License under WPCO	Works area of 3408	WT00038836-2021	Valid from 27 Sep 2021 to 30 Sep 2026
	Bill Account for disposal	Works area of 3408	A/C 7039063	Approval granted from EPD on 2 Dec 2020
	Construction Noise Permit (General Works)	Works area of 3408	GW-RS0020-22	Valid from 15 Jan 2022 to 30 Jun 2022
3503	Notification of Construction Work under APCO	Works area of 3503	459394	Receipt acknowledged by EPD on 28 Aug 2020
		Stockpiling area of 3503	459392	Receipt acknowledged by EPD on 28 Aug 2020
	Bill Account for disposal	Works area of 3503	A/C 7029665	Approval granted from EPD on 27 Dec 2017
3508	Notification of Construction Work under APCO	Works area of 3508	459017	Receipt acknowledged by EPD on 19 Aug 2020
			459469	Receipt acknowledged by EPD on 4 Sep 2020
		Works area of 3508 (Area J)	467132	Receipt acknowledged by EPD on 3 May 2021
	Registration as Chemical Waste Producer	Works area of 3508	WPN-5218-951-G2898-01	Completion of Registration on 28 Sep 2020
	Discharge License under WPCO	Works area of 3508	WT00037209-2020	Valid from 11 Mar 2021 to 31 Mar 2026
			WT00037523-2021	Valid from 1 Apr 2021 to 30 Apr 2026
			WT00037225-2020	Valid from 1 Apr 2021 to 30 Apr 2026
			WT00037549-2021	Valid from 1 Apr 2021 to 30 Apr 2026
	Bill Account for disposal	Works area of 3508	7038224	Approval granted from EPD on 8 Sep 2020
	Construction Noise Permit (General Works)	Works area of 3508	GW-RS0979-21	Valid from 19 Dec 2021 to 31 May 2022
		Works area of 3508	GW-RS0778-21	Valid from 15 Oct 2021 to 12 Apr 2022
		Works area of 3508 (Area 10)	GW-RS0016-22	Valid from 9 Jan 2022 to 3 Jul 2022
		Works area of 3508 (Special Case)	GW-RS0963-21	Valid from 17 Dec 2021 to 27 May 2022

Contract No.	Description	Location	Permit/ Reference No.	Status
3601	Notification of Construction Work under APCO Registration as Chemical Waste Producer Bill Account for disposal Construction Noise Permit (General Works)	Works area of 3508 (Special Case)	GW-RS0862-21	Valid from 13 Nov 2021 to 19 May 2022
		Works area of 3508 (Area 13)	GW-RS0999-21	Valid from 25 Dec 2021 to 31 May 2022
		Works area of 3601	451762	Receipt acknowledged by EPD on 10 Dec 2019
		Works area of 3601	WPN 7119-951-C4421-01	Completion of Registration on 9 Jan 2020
		Works area of 3601	A/C 7029991	Approval granted from EPD on 1 Feb 2018
3602	Notification of Construction Work under APCO Registration as Chemical Waste Producer Bill Account for disposal Construction Noise Permit (General Works)	Works area of 3601	GW-RS0899-21	Valid from 1 Dec 2021 to 31 May 2022
		Works area of 3602	421278	Receipt acknowledged by EPD on 18 Sep 2017
		Works area of 3602	WPN 5296-951-N2673-01	Completion of Registration on 9 Oct 2017
		Site office of 3602	WPN 5296-951-N2673-02	Completion of Registration on 11 Dec 2017
		Works area of 3602	A/C 7028942	Approval granted from EPD on 6 Oct 2017
3603	Notification of Construction Work under APCO Registration as Chemical Waste Producer Bill Account for disposal Construction Noise Permit (General Works)	Works area of 3602	GW-RS0650-21	Valid from 1 Oct 2021 to 1 Mar 2022
		Site office of 3603	433604	Receipt acknowledged by EPD on 16 May 2018
		Site office of 3603	5296-951-S4069-01	Completion of Registration on 22 Jan 2018
		Test Loop Site of 3603	8334-512-S4273-01	Completion of Registration on 17 Sep 2020
		Works area of 3603	A/C 7030002	Approval granted from EPD on 1 Feb 2018
3721	Notification of Construction Work under APCO Registration as Chemical Waste Producer Bill Account for disposal Construction Noise Permit (General Works)	Works area of 3603	GW-RS0878-21	Valid from 24 Nov 2021 to 23 May 2022
		Works area of 3721	448657	Receipt acknowledged by EPD on 02 Sep 2019
		Works area of 3721	WPN 5218-951-C4412-01	Completion of Registration on 9 Dec 2019
		Works area of 3721	A/C 7035234	Approval granted from EPD on 25 Sep 2019
		Works area of 3721	GW-RS0058-22	Valid from 31 Jan 2022 to 30 Jun 2022
3723	Notification of Construction	3723A	464440	Receipt acknowledged by EPD on 9 Feb 2021

Contract No.	Description	Location	Permit/ Reference No.	Status
	Work under APCO	3723B	464444	Receipt acknowledged by EPD on 9 Feb 2021
	Registration as Chemical Waste Producer	3723A	WPN 5218-951-T3920-01	Completion of Registration on 9 Feb 2021
		3723B	WPN 5218-951-T3921-01	Completion of Registration on 9 Feb 2021
	Discharge License under WPCO	Works area of 3723A & 3723B	WT00039451-2021	Valid from 28 Oct 2021 to 31 Oct 2023
	Bill Account for disposal	Works area of 3723A	A/C 7039755	Approval granted from EPD on 24 Feb 2021
		Works area of 3723B	A/C 7039754	Approval granted from EPD on 24 Feb 2021
	Construction Noise Permit (General Works)	Works area of 3723A & 3723B	GW-RS0697-21	Valid from 16 Sep 2021 to 13 Mar 2022
		Works area of 3723A & 3723B	GW-RS1013-21	Valid from 14 Jan 2022 to 13 Jul 2022
3728	Registration as Chemical Waste Producer	Works area of 3728	WPN 5111-951-S3467-03	Completion of Registration on 7 May 2021
	Discharge License under WPCO	Works area of 3728	WT00037809-2021	Valid from 27 Jul 2021 to 31 Jul 2026
	Bill Account for disposal	Works area of 3728	A/C 7039409	Approval granted from EPD on 22 Jan 2021
3733	Notification of Construction Work under APCO	Works area of 3733	472772	Receipt acknowledged by EPD on 18 Oct 2021
	Registration as Chemical Waste Producer	Works area of 3733	474728	Receipt acknowledged by EPD on 9 Dec 2021
	Bill Account for disposal	Works area of 3733	7041945	Approval granted from EPD on 21 Oct 2021
3801	Notification of Construction Work under APCO	Works area of 3801	430372	Receipt acknowledged by EPD on 2 Feb 2018
			435652	Receipt acknowledged by EPD on 16 Jul 2018
			451991	Receipt acknowledged by EPD on 18 Dec 2019
		Stockpiling area of 3801	450940	Receipt acknowledged by EPD on 13 Nov 2019
	Registration as Chemical Waste Producer	Works area of 3801	WPN 5296-951-C1169-53	Completion of Registration on 14 Aug 2018
	Discharge License under WPCO	Works and stockpiling area of 3801	WT00029535-2017	Valid from 30 Jul 2019 to 30 Nov 2022
		Stockpiling area of 3801	WT00037354-2021	Valid from 8 Mar 2021 to 31 Mar 2026
	Bill Account for disposal	Works area of 3801	A/C 7028254	Approval granted from EPD on 3 Jul 2017
	Construction Noise Permit (General Works)	Works area of 3801	GW-RS0634-21	Valid from 27 Aug 2021 to 26 Feb 2022 Superseded by GW-RS0132-22
		Works area of 3801	GW-RS0132-22	Valid from 27 Feb 2022 to 26 Aug 2022

Contract No.	Description	Location	Permit/ Reference No.	Status
3802	Construction Noise Permit (Special Case)	Works area of 3801 (Box Jacking)	GW-RS0103-22	Valid from 11 Feb 2022 to 8 May 2022
	Notification of Construction Work under APCO	Works area of 3802	458122	Receipt acknowledged by EPD on 14 Jul 2020
	Registration as Chemical Waste Producer	Works area of 3802	WPN 5218-951-G2895-01	Completion of Registration on 28 Aug 2020
		Works area of 3802 (Existing Airport)	WPN 5218-951-G2945-01	Completion of Registration on 29 Sep 2020
	Discharge License under WPCO	Works area of 3802	WT00037032-2020	Valid from 25 May 2021 to 31 May 2026
		Works area of 3802	WT00039092-2021	Valid from 30 Nov 2021 to 31 Nov 2026
	Bill Account for disposal	Works area of 3802	A/C 7037575	Approval granted from EPD on 15 Jun 2020
	Construction Noise Permit (General Works)	Works area of 3802	GW-RS0959-21	Valid from 13 Dec 2021 to 12 Jun 2022 Superseded by GW-RS0114-22
		Works area of 3802	GW-RS0114-22	Valid from 18 Feb 2022 to 13 Aug 2022
		Works area of 3802	GW-RS0888-21	Valid from 29 Nov 2021 to 19 May 2022
3901A	Notification of Construction Work under APCO	Works area of 3901A	466883	Receipt acknowledged by EPD on 26 Apr 2021
	Air Pollution Control (Furnaces, Ovens and Chimneys) (Installation and Alteration) Regulations	Works area of 3901A	EP/RS/0000443 053	Approval granted on 11 Dec 2020
	Specified Process license under APCO	Works area of 3901A	L-3-261(1)	Valid from 14 Sep 2020 to 13 Sep 2024
	Registration as Chemical Waste Producer	Works area of 3901A	WPN 5218-951-K3400-01	Completion of Registration on 17 Jul 2020
	Landfill disposal of waste concrete from batching plant	Works area of 3901A	EP195/01/18	Valid from 5 May 2021 to 2 Feb 2022 (Under renewal process)
	Bill Account for disposal	Works area of 3901A	A/C 7037889	Approval granted from EPD on 20 Jul 2020
	Construction Noise Permit (General Works)	Works area of 3901A	GW-RS0597-21	Valid from 7 Aug 2021 to 4 Feb 2022
		Works area of 3901A	GW-RS0059-22	Valid from 5 Feb 2022 to 4 Aug 2022
3901B	Notification of Construction Work under APCO	Works area of 3901B	466885	Receipt acknowledged by EPD on 26 Apr 2021
	Air Pollution Control (Furnaces,	Works area of 3901B	EP/RS/0000438 488	Approval granted on 26 Jun 2020

Contract No.	Description	Location	Permit/ Reference No.	Status
	Ovens and Chimneys) (Installation and Alteration) Regulations			
	Specified Process license under APCO	Works area of 3901B	L-3-262(1)	Valid from 17 Nov 2020 to 16 Nov 2024
	Registration as Chemical Waste Producer	Works area of 3901B	WPN 5218-951-G2880-01	Completion of Registration on 17 Jan 2020
	Bill Account for disposal	Works area of 3901B	A/C 7032417	Approval granted from EPD on 13 Nov 2018
	Construction Noise Permit (General Works)	Works area of 3901B	GW-RS0702-21	Valid from 16 Sep 2021 to 13 Mar 2022

Appendix E. Cumulative Statistics on Exceedances, Environmental Complaints, Notification of Summons and Status of Prosecutions

Statistics for Exceedances for 1-hour TSP, Noise, Water, Waste, CWD Monitoring

		Total no. recorded in the reporting period	Total no. recorded since the project commenced
1-hr TSP	Action	0	0
	Limit	0	0
Noise	Action	0	0
	Limit	0	0
Water	Action	0	0
	Limit	0	0
Waste	Action	1	1
	Limit	0	0
CWD	Action	0	0
	Limit	0	0

Remark: Exceedances, which are not project related, are not shown in this table.

Statistics for Complaints, Notifications of Summons and Prosecutions

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of Summons	Prosecutions
This reporting period	1	0	0
From 28 December 2015 to end of the reporting period	48	2	2
