



---

# Monthly EM&A Report (March 2024)

0185/21/ED/620 02

**Sai O Trunk Sewer Sewage Pumping Station**

Ref.: SHKSOSPSEM00\_0\_0107L.24

23 April 2024

By Fax (2827 0485)

Sun Hung Kai Properties Ltd.  
42/F., Sun Hung Kai Centre  
30 Harbour Road, Wan Chai, Hong Kong

Attention: Mr. Sunny Cheung

Dear Sir,

**Re: Sai O Trunk Sewer Sewage Pumping Station  
Environmental Permit No. EP-597/2021  
Monthly EM&A Report (March 2024)**

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for March 2024 (ET's ref.:0185/21/ED/0620 02) certified by the ET Leader and provided to us via e-mail on 23 April 2024.

We are pleased to inform you that we have no further comments on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 of EP-597/2021 and Section 12.4.1.1 of EM&A Manual for the captioned project.

The ET Leader is reminded that it is the ET's responsibility to ensure the report is timely submitted to the Director of Environmental Protection as per Conditions 3.4 of the EP-597/2021.

Thank you very much for your attention and please feel free to contact the undersigned should you require further information.

Yours sincerely,  
For and on behalf of  
Ramboll Hong Kong Ltd.



Y H Hui  
Independent Environmental Checker

|      |       |                             |                     |
|------|-------|-----------------------------|---------------------|
| c.c. | AECOM | Ms. Janice Tam / Mr. CK Man | (By Fax: 3894 5801) |
|      | Fugro | Mr. Calvin Leung            | (By Fax: 2450 6138) |
|      | SGJV  | Mr. Eddie Tse               | (By Fax: 3894 5801) |

Q:\Projects\SHKSOSPSEM00\02 Proj\_Mgt\02 Corr\SHKSOSPSEM00\_0\_0107L.24.docx

# Document Control


## Document Information

|                    |  |
|--------------------|--|
| Project Title      | Sai O Trunk Sewer Sewage Pumping Station |
| Document Title     | Monthly EM&A Report (March 2024)         |
| Fugro Project No.  | 0185/21                                  |
| Fugro Document No. | 0185/21/ED/620 02                        |
| Issue Number       | 02                                       |

## Client Information

|                |   |
|----------------|---|
| Client         | Light Time Investments Limited                                  |
| Client Address | 42/F, Sun Hung Kei Centre, 30 Harbour Road, Wan Chai, Hong Kong |
| Client Contact | Mr. Sunny Cheung  |

## Environmental Team

| Initials | Name              | Role                      | Signature   |
|----------|-------------------|---------------------------|---|
| MP       | Calvin M.P. Leung | Environmental Team Leader |   |
| KH       | Toby K.H. Wan     | Environmental Consultant  |  |
| JT       | Jhomar P. Tillo   | Ecologist                 |  |

---

## EXECUTIVE SUMMARY

- i. This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Sai O Trunk Sewer Sewage Pumping Station. Light Time Investments Limited has appointed Fugro Technical Services Limited (FTS) to undertake the Environmental Team services for the project and implement the EM&A works.
- ii. This is the 26<sup>th</sup> Monthly EM&A Report for the Project which summaries findings of the EM&A programme during the reporting period from 1<sup>st</sup> March 2024 to 31<sup>st</sup> March 2024.

### **Breaches of Environmental Quality Performance Limits (Action & Limit levels)**

- iii. No Action and Limit Level exceedance was recorded for air quality and construction noise monitoring in the reporting month.
- iv. No corrective actions were required according to the Event-Action Plans.

### **Complaint Log**

- v. No complaints were received in the reporting period.

### **Notifications of any Summons and Successful Prosecutions**

- vi. No notifications of summons and prosecutions were received in the reporting period.

### **Reporting Change**

- vii. There were no reporting changes during the reporting month.

### **Future Key Issues**

- viii. The main works will be anticipated in the next month are as follow:

#### ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

#### E&M Works and OP

- E&M works – pump room below and above ground
- E&M works – external



## Contents

|           |   |           |
|-----------|---|-----------|
| <b>1.</b> | <b>INTRODUCTION</b>   | <b>8</b>  |
| 1.1       | Background  | 8         |
| 1.2       | Project Organization  | 9         |
| 1.3       | Construction Programme and Activities   | 10        |
| 1.4       | Works undertaken during the month   | 10        |
| 1.5       | Status of Environmental Licences, Notification and Permits                              | 11        |
| <b>2.</b> | <b>AIR QUALITY</b>  | <b>12</b> |
| 2.1       | Monitoring Requirement  | 12        |
| 2.2       | Monitoring Equipment  | 12        |
| 2.3       | Monitoring Parameters and Frequency   | 12        |
| 2.4       | Monitoring Methodology  | 13        |
| 2.5       | Maintenance and Calibration   | 14        |
| 2.6       | Monitoring Locations  | 14        |
| 2.7       | Monitoring Results  | 14        |
| <b>3.</b> | <b>NOISE</b>  | <b>16</b> |
| 3.1       | Monitoring Requirement  | 16        |
| 3.2       | Monitoring Equipment  | 16        |
| 3.3       | Monitoring Parameters and Frequency   | 16        |
| 3.4       | Monitoring Methodology  | 17        |
| 3.5       | Maintenance and Calibration   | 17        |
| 3.6       | Monitoring Locations  | 18        |
| 3.7       | Monitoring Results  | 18        |
| 3.8       | Comparison of Noise Monitoring data with EIA Predictions                                | 19        |
| <b>4.</b> | <b>SITE INSPECTION AND AUDIT</b>  | <b>20</b> |
| 4.1       | Site Inspection   | 20        |
| 4.2       | Advice on the Solid and Liquid Waste Management Status                                  | 20        |
| <b>5.</b> | <b>NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS</b> | <b>21</b> |
| 5.1       | Non-compliance (Exceedances of AL levels)   | 21        |
| 5.2       | Complaints, Notification of Summons and Prosecution                                     | 21        |
| <b>6.</b> | <b>IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURE</b>                        | <b>22</b> |
| 6.1       | Implementation Status   | 22        |
| <b>7.</b> | <b>FUTURE KEY ISSUES</b>  | <b>23</b> |
| 7.1       | Construction Programme for the Next Month   | 23        |
| 7.2       | Key Issues for the Coming Month   | 23        |
| 7.3       | Monitoring Schedules for the Next Month   | 23        |

|           |                                      |           |
|-----------|--------------------------------------|-----------|
| <b>8.</b> | <b>CONCLUSION AND RECOMMENDATION</b> | <b>24</b> |
| 8.1       | Conclusions                          | 24        |
| 8.2       | Comment and Recommendations          | 24        |

---

## Tables

|                  |   |
|------------------|---|
| <b>Table 1.1</b> | Contact Information of Key Personnel                      |
| <b>Table 1.2</b> | Environmental Licenses, Notification and Permits Summary  |
| <b>Table 2.1</b> | Air Quality Monitoring Equipment                          |
| <b>Table 2.2</b> | Monitoring Parameters and Frequencies of Noise Monitoring |
| <b>Table 2.3</b> | Air Quality Monitoring Locations                          |
| <b>Table 2.4</b> | Summary of Air Quality Monitoring Results                 |
| <b>Table 3.1</b> | Construction Noise Monitoring Equipment                   |
| <b>Table 3.2</b> | Monitoring Parameters and Frequencies of Noise Monitoring |
| <b>Table 3.3</b> | Construction Noise Monitoring Location                    |
| <b>Table 3.4</b> | Summary of Construction Noise Monitoring Results          |
| <b>Table 3.5</b> | Comparison of Noise monitoring data with EIA predictions  |

---

## Figures

**Figure 1.1** Location of the proposed Sai O Trunk Sewer SPS

**Figure 2.1** Air Quality Monitoring Location

**Figure 3.1** Noise Monitoring Locations

---

## Appendices

**Appendix A** Project Organization Chart

**Appendix B** Construction Programme

**Appendix C** Equipment Calibration Certificates

**Appendix D** Environmental Monitoring Schedule

**Appendix E** Air Quality & Construction Noise Monitoring Results

**Appendix F** Air Quality & Construction Noise Monitoring Graphs

**Appendix G** Action and Limit Level

**Appendix H** Event and Action Plan

**Appendix I** Weather and Meteorological Conditions during Reporting Month

**Appendix J** Wind Data

**Appendix K** Summary of Site Environmental Audit in the Reporting Month

**Appendix L** Waste Flow Table

**Appendix M** Cumulative Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

**Appendix N** Implementation Status of Environment Mitigation Measures (Construction Phase)

**Appendix O** Outstanding Issues and Deficiencies

# 1. INTRODUCTION

## 1.1 Background

- 1.1.1 The proposed Sai O Trunk Sewer Sewage Pumping Station (Sai O Trunk Sewer SPS) is a part of Public Works Programme Item 4125DS - Tolo Harbour Sewerage of Unsewered Areas, Stage II, is a core component of the proposed trunk sewerage system in Ma On Shan along Sai Sha Road. It is required to receive all sewage flows along Sai Sha Road from Kei Ling Ha Lo Wai to Cheung Muk Tau and the adjacent residential development, health care institution and education institutions, and then convey the sewage to Sha Tin Sewage Treatment Works.
- 1.1.2 Based on the latest design, the installed capacity per day of the proposed Sai O Trunk Sewer SPS is about 20,600m<sup>3</sup> for coping with the sewerage needs of both existing and future developments. Location of the proposed Sai O Trunk Sewer SPS is shown in **Figure 1.1**.
- 1.1.3 The proposed Sai O Trunk Sewer SPS include the following main components:
- Loading/unloading bay
  - Inlet chamber
  - Coarse screen channel
  - Distribution chamber
  - Wet wells
  - Valve chamber
  - Emergency storage tank
  - Deodorizing unit
  - Switch room
  - Transformer room
- 1.1.4 The Project is a designated project under Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap. 499) for which Environmental Impact Assessment (EIA) report and Environmental Monitoring and Audit (EM&A) Manual was approved by EPD (Register No.: AEIAR-230/2021) on 4 June 2021. The Environmental Permit (EP) (EP No. EP-597/2021) was issued by EPD on 28 September 2021.
- 1.1.5 Fugro Technical Services Limited (FTS) has been appointed as the Environmental Team (ET) by Light Time Investments Limited to undertake the Environmental Team services for the Project and implement the EM&A works under Sai O Trunk Sewer Sewage Pumping Station (hereinafter referred as “the Project”).

- 1.1.6 This is the 25<sup>th</sup> Monthly EM&A report to document the findings of site inspection activities and EM&A programme for this project from 1<sup>st</sup> March 2024 to 31<sup>st</sup> March 2024 (reporting period) and is submitted to fulfil Condition 3.4 of the EP and Section 12.4 of the EM&A Manual. According to Condition 4 of the EP, electronic reporting is provided on the internet website to facilitate public inspection of the report.

## 1.2 Project Organization

- 1.2.1 The Project Organization structure is shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 – Contact Information of Key Personnel

| Party   | Position                          | Name             | Telephone |
|---|-----------------------------------|------------------|-----------|
| Project Proponent (PP)<br>(Light Time Investments Ltd.)             | Senior Project Manager            | Mr. Sunny Cheung | 3894 5934 |
| Engineer's Representative (ER)<br>(AECOM Asia Co. Ltd.)             | Senior Resident Engineer          | Mr. C.K. Man     | 3894 5919 |
| Independent Environmental Checker (IEC)<br>(Ramboll Hong Kong Ltd.) | Independent Environmental Checker | Mr. Y.H. Hui     | 3465 2888 |
| Contractor<br>(Sanfield-Gammon Construction JV Company Ltd.)        | Environmental Officer             | Ms. Carrie Kwan  | 3894 5816 |
| Environmental Team (ET)<br>(Fugro Technical Services Ltd.)          | Environmental Team Leader (ETL)   | Mr. Calvin Leung | 3565 4441 |

### 1.3 Construction Programme and Activities

1.3.1 The construction programme of this project is shown in **Appendix B**.

### 1.4 Works undertaken during the month

1.4.1 Major construction activities were undertaken in the reporting month were:

#### ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

#### E&M Works and OP

- E&M works – pump room below and above ground
- E&M works – external

## 1.5 Status of Environmental Licences, Notification and Permits

- 1.5.1 A summary of the relevant permits, licenses and/or notifications on environmental protection for this project is presented in **Table 1.2**.

Table 1.2 – Environmental Licenses, Notification and Permits Summary

| Permit/ Notification/ License                                     | Reference No      | Valid From  | Valid Till  |
|---|-------------------|-------------|-------------|
| Environmental Permit  | EP-597/2021       | 28-Sep-2021 | NA          |
| Notification of Construction Works under APCO                     | 494463            | 18-Apr-2018 | 31-Dec-2024 |
| Billing Account under Construction Waste Disposal Charging Scheme | 7031695           | 28-Aug-2018 | NA          |
| Effluent Discharge License under WPCO                             | WT00040139-2021   | 11-Mar-2022 | 31-Mar-2027 |
| Chemical Waste Producer Registration                              | 8334-741-S4115-01 | 14-Aug-2018 | NA          |
| Construction Noise Permit   | GW-RN0205-24      | 26-Feb-2024 | 25-May-2024 |

Notes:

NA = Not Applicable



## 2. AIR QUALITY

### 2.1 Monitoring Requirement

- 2.1.1 In accordance with the EM&A Manual, 1-hour Total Suspended Particulates (TSP) levels should be measured at the designated air quality monitoring station to ensure that any deteriorating air quality could be readily detected and timely action shall be undertaken to rectify such situation. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days when the highest dust impact occurs.

### 2.2 Monitoring Equipment

- 2.2.1 1-hour TSP air quality monitoring was performed using High Volume Sampler (HVS) deployed at the designated monitoring station. The HVS shall meet all the requirements of the EM&A Manual.
- 2.2.2 Wind data monitoring equipment is provided at the conspicuous locations for logging wind speed and wind direction near to the air quality monitoring location. The equipment installation location is agreed with the ER and the IEC.
- 2.2.3 The model of the air quality monitoring equipment used is summarized in **Table 2.1**.

Table 2.1 – Air Quality Monitoring Equipment

| Item | Brand        | Model         | Equipment                 | Serial No. |
|------|--------------|---------------|---------------------------|------------|
| 1    | Tisch        | TE-5170 (TSP) | High Volume Sampler       | HVS-05     |
|      |              | TE-300-310X   | -Mass Flow Controller     | 3088       |
|      |              | TE-5005X      | -Blower Motor Assembly    | 2083       |
|      |              | TE-5007X      | -Mechanical Timer         | 5159       |
|      |              | TE-5009X      | -Continuous Flow Recorder | 5483       |
| 2    | Global Water | GL500-7-2     | Wind Station              | WS-03      |
| 3    | Tisch        | TE-5025A      | Calibration Kit           | 2456       |

### 2.3 Monitoring Parameters and Frequency

- 2.3.1 The parameters and frequencies of impact noise monitoring is summarized in **Table 2.2**.

Table 2.2 – Monitoring Parameters and Frequencies of Air Quality Monitoring

| Parameter  | Frequency   |
|------------|---|
| 1-hour TSP | At least three times every 6 days when the highest dust impact occurs |

## 2.4 Monitoring Methodology

### HVS Installation

2.4.1 The following guidelines were adopted during the installation of HVS:

- i. A horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
- ii. Two samplers shall be placed less than 2 meters apart;
- iii. The distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
- iv. A minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;
- v. A minimum of 2 metres of separation from any supporting structure, measured horizontally is required;
- vi. No furnace or incinerator flue is nearby;
- vii. Airflow around the sampler is unrestricted;
- viii. The sampler is more than 20 metres from the dripline;
- ix. Any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
- x. Permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
- xi. A secured supply of electricity is needed to operate the samplers.

### Operating / Analytical Procedures

- 2.4.2 Prior to the commencement of the dust sampling, the flow rate of the HVS shall be properly set. The flow rate shall be indicated on the flow rate chart. The power supply should be checked to ensure the proper functioning of the sampler. The sampler is recommended to be operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 2.4.1 The filter holding frame should be removed by loosening the four nuts and placing carefully a weighted and conditioned filter at the centre with the stamped number upwards on a supporting screen.
- 2.4.2 The filter should be aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. The filter holding frame should be tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.

- 2.4.3 A programmed timer should be used to control the duration of operation. Information should be recorded on the record sheet, which included the starting time, the weather condition and the filter number.
- 2.4.4 After sampling process is finished, the filter should be removed and sent to the laboratory for weighting. The elapsed time should also be recorded.
- 2.4.5 All filter papers should be equilibrated in a conditioning environment for 24 hours before weighting. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than  $\pm 3^{\circ}\text{C}$ ; the relative humidity (RH) should be  $< 50\%$  and not vary by more than  $\pm 5\%$ . A convenient working RH is 40%.

## 2.5 Maintenance and Calibration

- 2.5.1 The high-volume motors and their accessories should be properly maintained, including routine motor brushes replacement and electrical wiring checking, to ensure that the equipment and a continuous power supply were in good working condition.
- 2.5.2 Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bimonthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The calibration certificate for the HVS is provided in **Appendix C**.

## 2.6 Monitoring Locations

- 2.6.1 In accordance with the EM&A Manual, air quality monitoring should be carried out at a designated monitoring location.
- 2.6.2 As limitation of stable electricity supply & safety concern could not be obtained from the designated dust monitoring location, an alternative monitoring location (CA\_M1(a)) was proposed to measure 1-hour TSP levels in accordance with EP Condition 3.1 & Section 2.2.1.20 of the EM&A manual. The alternative monitoring location (CA\_M1(a)) was approved by EPD on 15 December 2021.
- 2.6.3 The air quality monitoring location summarised in **Table 2.3** and shown in **Figure 2.1**.

Table 2.3 – Air Quality Monitoring Locations

| Monitoring Location ID | Location   |
|------------------------|--|
| CA_M1(a)               | Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters |

## 2.7 Monitoring Results

- 2.7.1 The schedule of air quality monitoring in reporting month is provided in **Appendix D**.
- 2.7.2 The monitoring data of 1-hr TSP are summarized in **Table 2.4**. The Detailed air quality monitoring results & graphs are presented in **Appendix E** & **Appendix F** respectively.

Table 2.4 – Summary of Air Quality Monitoring Results

| Monitoring Station | Average ( $\mu\text{g}/\text{m}^3$ ) | Range ( $\mu\text{g}/\text{m}^3$ ) | Action Level ( $\mu\text{g}/\text{m}^3$ ) | Limit Level ( $\mu\text{g}/\text{m}^3$ ) |
|--------------------|--------------------------------------|------------------------------------|---|--|
| 1-hour TSP         |                                      |                                    |   |  |
| CA_M1(a)           | 179.4                                | 75.6 – 334.9                       | 339                                       | 500                                      |

- 2.7.3 No Action and Limit level exceedance was recorded in the reporting month.
- 2.7.4 No effect that arose from the other special phenomena and work progress of the concerned site was noted during the current monitoring month.
- 2.7.5 The Action and Limit Levels for impact air quality monitoring have been set and are presented in **Appendix G**.
- 2.7.6 The Event and Action Plan for Air Quality is given in **Appendix H**.
- 2.7.7 The weather conditions during the monitoring are provided in **Appendix I**.
- 2.7.8 The wind data obtained from the on-site wind station during the reporting period is provided in **Appendix J**.

### 3. NOISE

#### 3.1 Monitoring Requirement

- 3.1.1 In accordance with the EM&A Manual, Leq (30min) monitoring is conducted at least once a week when there are Project-related construction activities being undertaken within a radius of 300 m from the monitoring stations. The monitoring is conducted during the construction phase between 0700 and 1900 on normal weekdays at the designated monitoring locations.

#### 3.2 Monitoring Equipment

- 3.2.1 As referred to the requirements of the Technical Memorandum (TM) issued under the NCO, the sound level meters in compliance with the International Electro technical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications should be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement, the accuracy of the sound level meter should be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The measurements may be accepted as valid only if the difference between calibration levels obtained before and after the noise measurement is less than 1.0 dB (94 dB  $\pm$  0.1 dB).
- 3.2.2 The model of the noise monitoring equipment used is summarized in **Table 3.1**.

Table 3.1 – Construction Noise Monitoring Equipment

| Item | Brand        | Model          | Equipment                     | Serial No. |
|------|--------------|----------------|-------------------------------|------------|
| 1    | Casella      | CEL-63X Series | Integrating Sound Level Meter | 1488300    |
| 2    | Casella      | CEL-120/1      | Calibrator                    | 1677126    |
| 3    | Smart Sensor | AR816          | Anemometer                    | AM-001     |

#### 3.3 Monitoring Parameters and Frequency

- 3.3.1 The parameters and frequencies of impact noise monitoring is summarized in **Table 3.2**.

Table 3.2 – Monitoring Parameters and Frequencies of Noise Monitoring

| Parameter   | Frequency   |
|---|---|
| LAeq (30 min)<br>(L10 and L90 will be recorded for reference) | At each station at 0700-1900 hours on normal weekdays at a frequency of once a week when construction activities are underway |

### 3.4 Monitoring Methodology

3.4.1 Noise measurement should be conducted as the following procedures:

- The monitoring station will set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 1.2m above the ground. (In case façade measurement is not feasible on-site, a free field correction of +3dB(A) will be applied.)
- The battery condition was checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time will set as follows:
  - frequency weighting: A
  - time weighting: Fast
  - measurement time: 30 minutes
- Prior to and after noise measurement, the meter shall be calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement will be considered invalid and repeat of noise measurement is required after re-calibration or repair of the equipment.
- Noise measurement should be paused during periods of high intrusive noise if possible and observation shall be recorded when intrusive noise is not avoided.
- Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s. Calibration certificate of the anemometer is provided in **Appendix C**.

### 3.5 Maintenance and Calibration

3.5.1 Maintenance and calibration procedures should also be carried out, including:

- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory.
- Relevant calibration certificates are provided in **Appendix C**.

### 3.6 Monitoring Locations

3.6.1 In accordance with the EM&A Manual, noise monitoring should be carried out at 2 designated monitoring locations.

3.6.2 The noise monitoring locations are summarised in **Table 3.3** and shown in **Figure 3.1**.

Table 3.3 – Construction Noise Monitoring Location

| Monitoring Location ID | Location   | Measurements |
|------------------------|--|--------------|
| CN_M1                  | In front of the HKBTs Staff & Students Quarters          | Free Field   |
| CN_M2                  | In front of the HKBTs Administration and Education Block | Façade       |

Note: Correction of +3 dB(A) shall be made to the free field measurements.

### 3.7 Monitoring Results

3.7.1 The schedule of noise monitoring in reporting month is provided in **Appendix D**.

3.7.2 The noise monitoring data are summarized in **Table 3.4**. The Detailed noise monitoring results & graphs are presented in **Appendix E** & **Appendix F** respectively.

Table 3.4 – Summary of Construction Noise Monitoring Results

| Frequency and Period                            | Location | Corrected L <sub>Aeq</sub> |                 | Action Level                              | Limit Level   |
|---|----------|----------------------------|-----------------|---|---|
|   |          | Range (dB(A))              | Average (dB(A)) |   |   |
| 0700-1900 hours in normal weekdays LAeq (30min) | CN_M1    | 57.8 – 65.1                | 62.7            | When one documented complaint is received | 70dB(A) during normal teaching period and examination periods 65 dB(A) during |
|   | CN_M2    | 50.6 – 60.4                | 57.6            |   |   |

Remark:

1. CN\_M1: Free-field measurement (+3 dB(A) correction has been applied).

3.7.3 No Action / Limit Level exceedance of location CN\_M1 & CN\_M2 was recorded for construction noise in the reporting month.

3.7.4 Construction Noise and Road traffic noise along Nin Ming Road was observed at CN\_M1 & CN\_M2 during the monitoring month. No effect that arose from the other special phenomena was noted during the current monitoring month.

3.7.5 The Action and Limit Levels for Construction Noise have been set and are presented in **Appendix G**.

3.7.6 The Event and Action Plan for Construction Noise is given in **Appendix H**.

3.7.7 No raining and wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation. The weather conditions during the monitoring month are provided in **Appendix I**.

3.8 Comparison of Noise Monitoring data with EIA Predictions

3.8.1 The noise monitoring data was compared with the EIA predictions as summarized in **Table 3.5**.

Table 3.5 – Comparison of Noise monitoring data with EIA predictions

| Monitoring Station | EIA ID | Maximum Predicted Mitigated Construction Noise Level<br>Leq (30min) dB(A) | Maximum Construction Noise Level in March 2024<br>Leq (30min) dB(A) |
|--------------------|--------|---|---|
| CN_M1              | N1b    | 72  | 62.1  |
| CN_M2              | N2     | 66  | 60.4  |

Notes:  
Predicted Construction Noise Levels extracted from Table 4.8 of EIA Report, AEIAR-230/2021

3.8.2 The construction noise monitoring results at CN\_M1 and CN\_M2 were below the Maximum Predicted mitigated Construction Noise Level in the approved Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-230/2021).



## 4. SITE INSPECTION AND AUDIT

### 4.1 Site Inspection

- 4.1.1 Site audits were carried out by ET on weekly basis to monitor the implementation of proper environmental management practices and mitigation measures in the Project site.
- 4.1.2 In the reporting month, 4 site inspections were carried out on 4, 11, 18 and 25 March 2024.
- 4.1.3 No outstanding issues were reported during the reporting month. The Site Environmental Audit are summarized in **Appendix K**.

### 4.2 Advice on the Solid and Liquid Waste Management Status

- 4.2.1 The Contractor registered as a chemical waste producer for the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.
- 4.2.2 The monthly summary of waste flow table is detailed in **Appendix L**.
- 4.2.3 If off-site disposal is required, the excavated marine mud from the land-based works shall be disposed of at the designated disposal sites within Hong Kong as allocated by the Marine Fill Committee or other locations as agreed by the Director. The Contractor shall ensure no spilling and overflowing of materials during loading / unloading / transportation is allowed.
- 4.2.4 The Contractor was reminded that chemical waste should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packing, Labelling and Storage of Chemical Waste.

## 5. NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

### 5.1 Non-compliance (Exceedances of Action & Limit levels)

- 5.1.1 No Action and Limit Level exceedance was recorded for 1-hr TSP level at CA\_M1(a) in the reporting month.
- 5.1.2 No Action / Limit Level exceedance was recorded for construction noise at CN\_M1 & CN\_M2 in the reporting month.

### 5.2 Complaints, Notification of Summons and Prosecution

- 5.2.1 No environmental complaint, notification of summons and successful prosecution were received in the reporting month.
- 5.2.2 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix M**.
- 5.2.3 No corrective actions were required.

## 6. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURE

### 6.1 Implementation Status

The Contractor had implemented environmental mitigation measures and requirements as stated in the EIA Report, the EP and EM&A Manual. **Appendix N** summarized the Implementation Status of Environment Mitigation Measures.

## 7. FUTURE KEY ISSUES

### 7.1 Construction Programme for the Next Month

#### ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

#### E&M Works and OP

- E&M works – pump room below and above ground
- E&M works – external

### 7.2 Key Issues for the Coming Month

- 7.2.1 Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, waste management, and landscape and visual impact issues.

### 7.3 Monitoring Schedules for the Next Month

- 7.3.1 The tentative schedule for environmental monitoring in the coming month is provided in **Appendix D**.

## 8. CONCLUSION AND RECOMMENDATION

### 8.1 Conclusions

- 8.1.1 1-hour TSP impact monitoring was carried out in the reporting month. No Action and Limit Level exceedance was recorded in the reporting month.
- 8.1.2 Construction noise monitoring was carried out in the reporting month. No Action / Limit Level exceedance at CN\_M1 & CN\_M2 was recorded during the period.
- 8.1.3 Four environmental site inspections were carried out in the reporting month. No recommendations on mitigation measure was given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.4 Two landscape and visual site audits were carried out in the reporting month. Recommendations on mitigation measures for Permit/ Licenses were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.5 Referring to the Contractor's information, no environmental complaint, notification of summons and successful prosecution was received in the reporting month.

### 8.2 Comment and Recommendations

- 8.2.1 The recommended environmental mitigation measures, as proposed in the EIA report and EM&A Manual shall be effectively implemented to minimize the potential environmental impacts from the Project. The EM&A programme would effectively monitor the environmental impacts generated from the construction activities and ensure the proper implementation of mitigation measures.

- 8.2.2 **According to the environmental site inspections performed in the reporting month, the following recommendations were provided:**

#### Air Quality Impact

- No specific observation was identified in the reporting month.

#### Construction Noise Impact

- No specific observation was identified in the reporting month.

#### Water Quality Impact

- No specific observation was identified in the reporting month.

#### Chemical Waste and Waste Management

- No specific observation was identified in the reporting month.

#### Landscape and Visual Impact

- No specific observation was identified in the reporting month.


#### Permit/ Licenses

- No specific observation was identified in the reporting month.

## Figure 1.1

---

Location of the proposed Sai O Trunk  
SPS

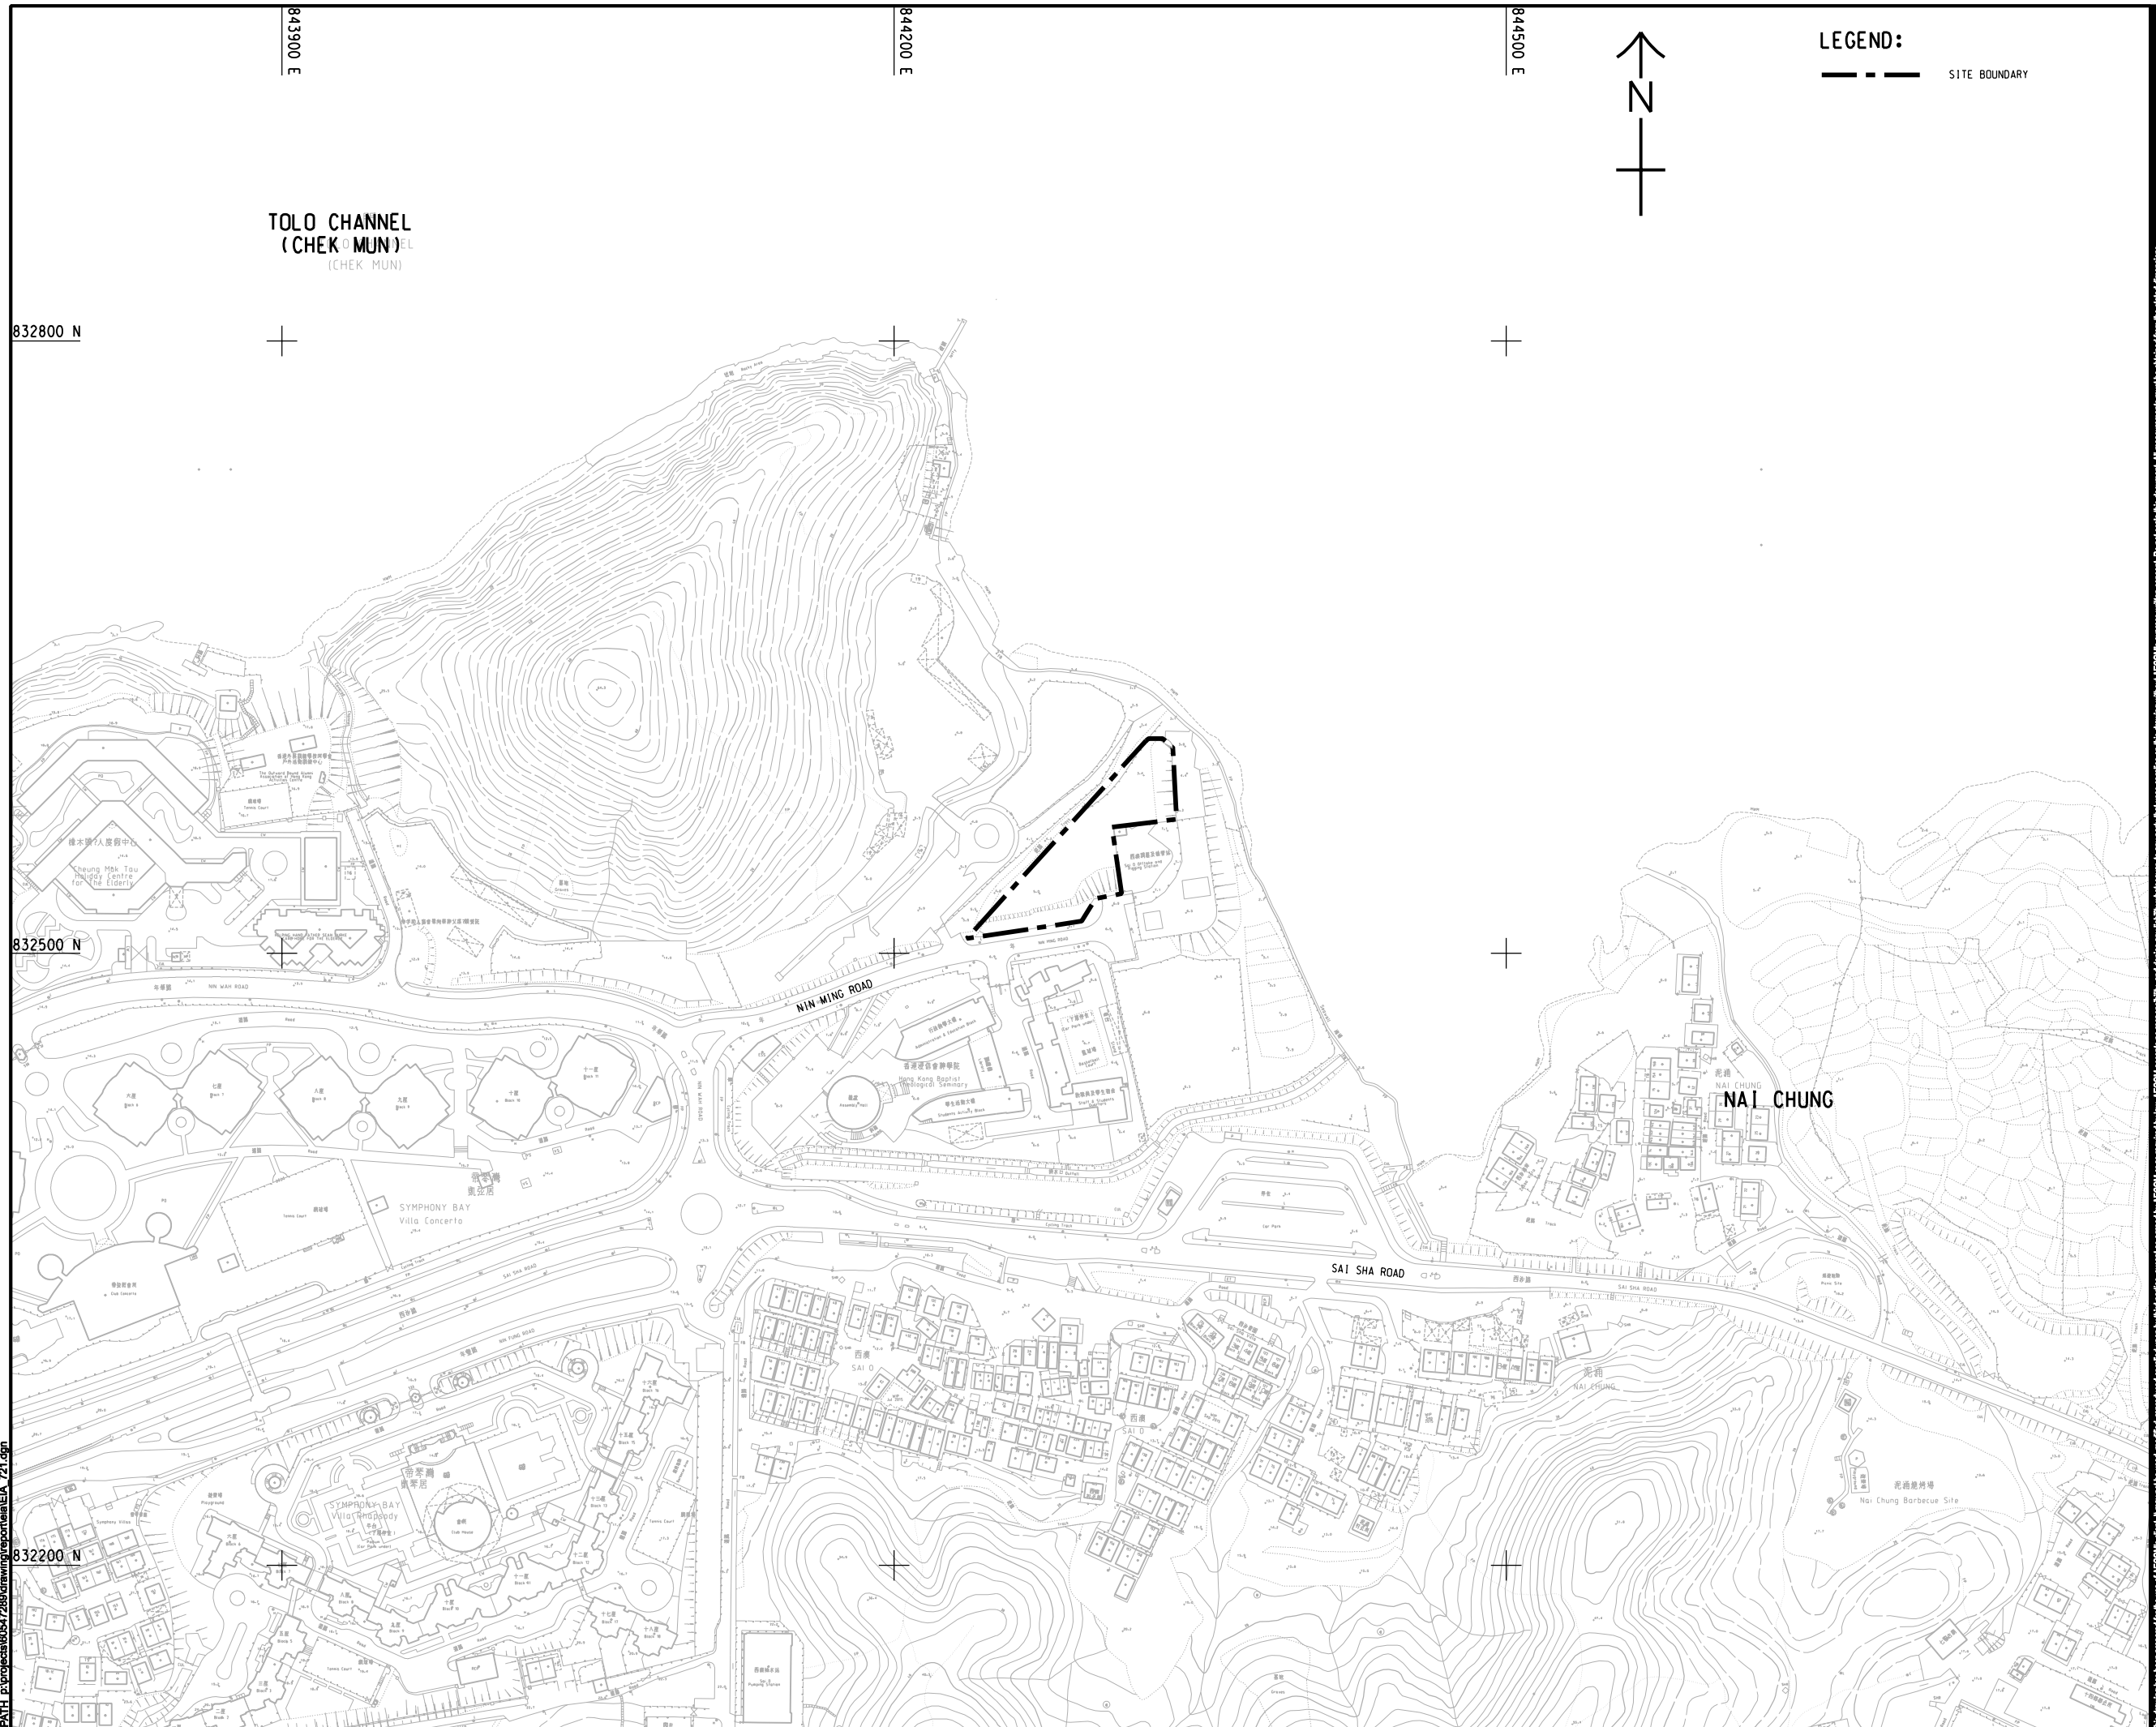

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

**AECOM**

## PROJECT

**TOLO HARBOUR  
SEWERAGE OF  
UNSEWERED AREAS  
STAGE 2 -  
INVESTIGATION, DESIGN  
AND CONSTRUCTION**

**CLIENT**  
業主



**CONSULTANT**  
工程顧問公司

**AECOM Asia Company Ltd.**  
**www.aecom.com**

**SUB-CONSULTANTS**  
分判工程顧問公司

**ISSUE/REVISION**

[illegible]

| I/R<br>修訂 | DATE<br>日期 | DESCRIPTION<br>內容摘要 | CHK<br>複核 |
|-----------|------------|---------------------|-----------|
|-----------|------------|---------------------|-----------|

**STATUS**

**SCALE**

**A1 1 : 1500**

**DIMENSION UNIT**  
尺寸單位

METRES

## KEY PLAN

PROJECT NO.  
項目編號

60547289

**SHEET TITLE**  
圖紙名稱

### LOCATION OF THE PROPOSED SAI O TRUNK SEWER SEWAGE PUMPING STATION

**SHEET NUMBER**  
圖紙編號

60547289/EM&amp;A/FIGURE 1.1

## Figure 2.1

---

Air Quality Monitoring Location



ISO A1 594mm x 841mm  
Approved:  
Checked:  
Designer:  
Project Management Initials:  
Plot File by: ZHUJUNZ 2020/12/21  
PATH P:\PROJECTS\60547289\DRAWING\Report\EA\EA\_731.dgn



**LEGEND:**

- SITE BOUNDARY
- 500m ASSESSMENT AREA
- REPRESENTATIVE AIR SENSITIVE RECEIVER
- ✗ CA\_M1(a) PROPOSED AIR QUALITY MONITORING POINT DURING CONSTRUCTION PHASE

**AECOM**

**PROJECT**  
項目

**TOLO HARBOUR SEWERAGE OF UNSEWERED AREAS STAGE 2 - INVESTIGATION, DESIGN AND CONSTRUCTION**

**CLIENT**  
業主

**渠務署**  
Drainage Services Department

**CONSULTANT**  
工程顧問公司

AECOM Asia Company Ltd.  
www.aecom.com

**SUB-CONSULTANTS**  
分判工程顧問公司

| ISSUE/REVISION |      |                |      |
|----------------|------|----------------|------|
| 修訂             |      |                |      |
|                |      |                |      |
|                |      |                |      |
|                |      |                |      |
|                |      |                |      |
|                |      |                |      |
|                |      |                |      |
| IR             | DATE | DESCRIPTION    | CHK. |
| 修訂             | 日期   | 修改描述           | 校核   |
| STATUS         |      |                |      |
| 校核             |      |                |      |
| SCALE          |      | DIMENSION UNIT |      |
| 比例             |      | 單位             |      |
| A1 1 : 2000    |      | METRES         |      |
| KEY PLAN       |      |                |      |
| 索引圖            |      |                |      |

**PROJECT NO.**  
項目編號

60547289

**CONTRACT NO.**  
合約編號

**SHEET TITLE**  
圖紙名稱

LOCATIONS OF PROPOSED DUST MONITORING POINT

**SHEET NUMBER**  
圖紙編號

60547289/EM&A/FIGURE 2.1

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.


## Figure 3.1

---

Noise Monitoring Locations



ISO A1 594mm x 841mm  
Approved:  
Checked:  
Designer:  
Project Management Initials:  
Pld File by: ZHUNZ 2020/10/28  
PATH P:\p\60547289\DRAWING\Report\EM&A 741.dgn

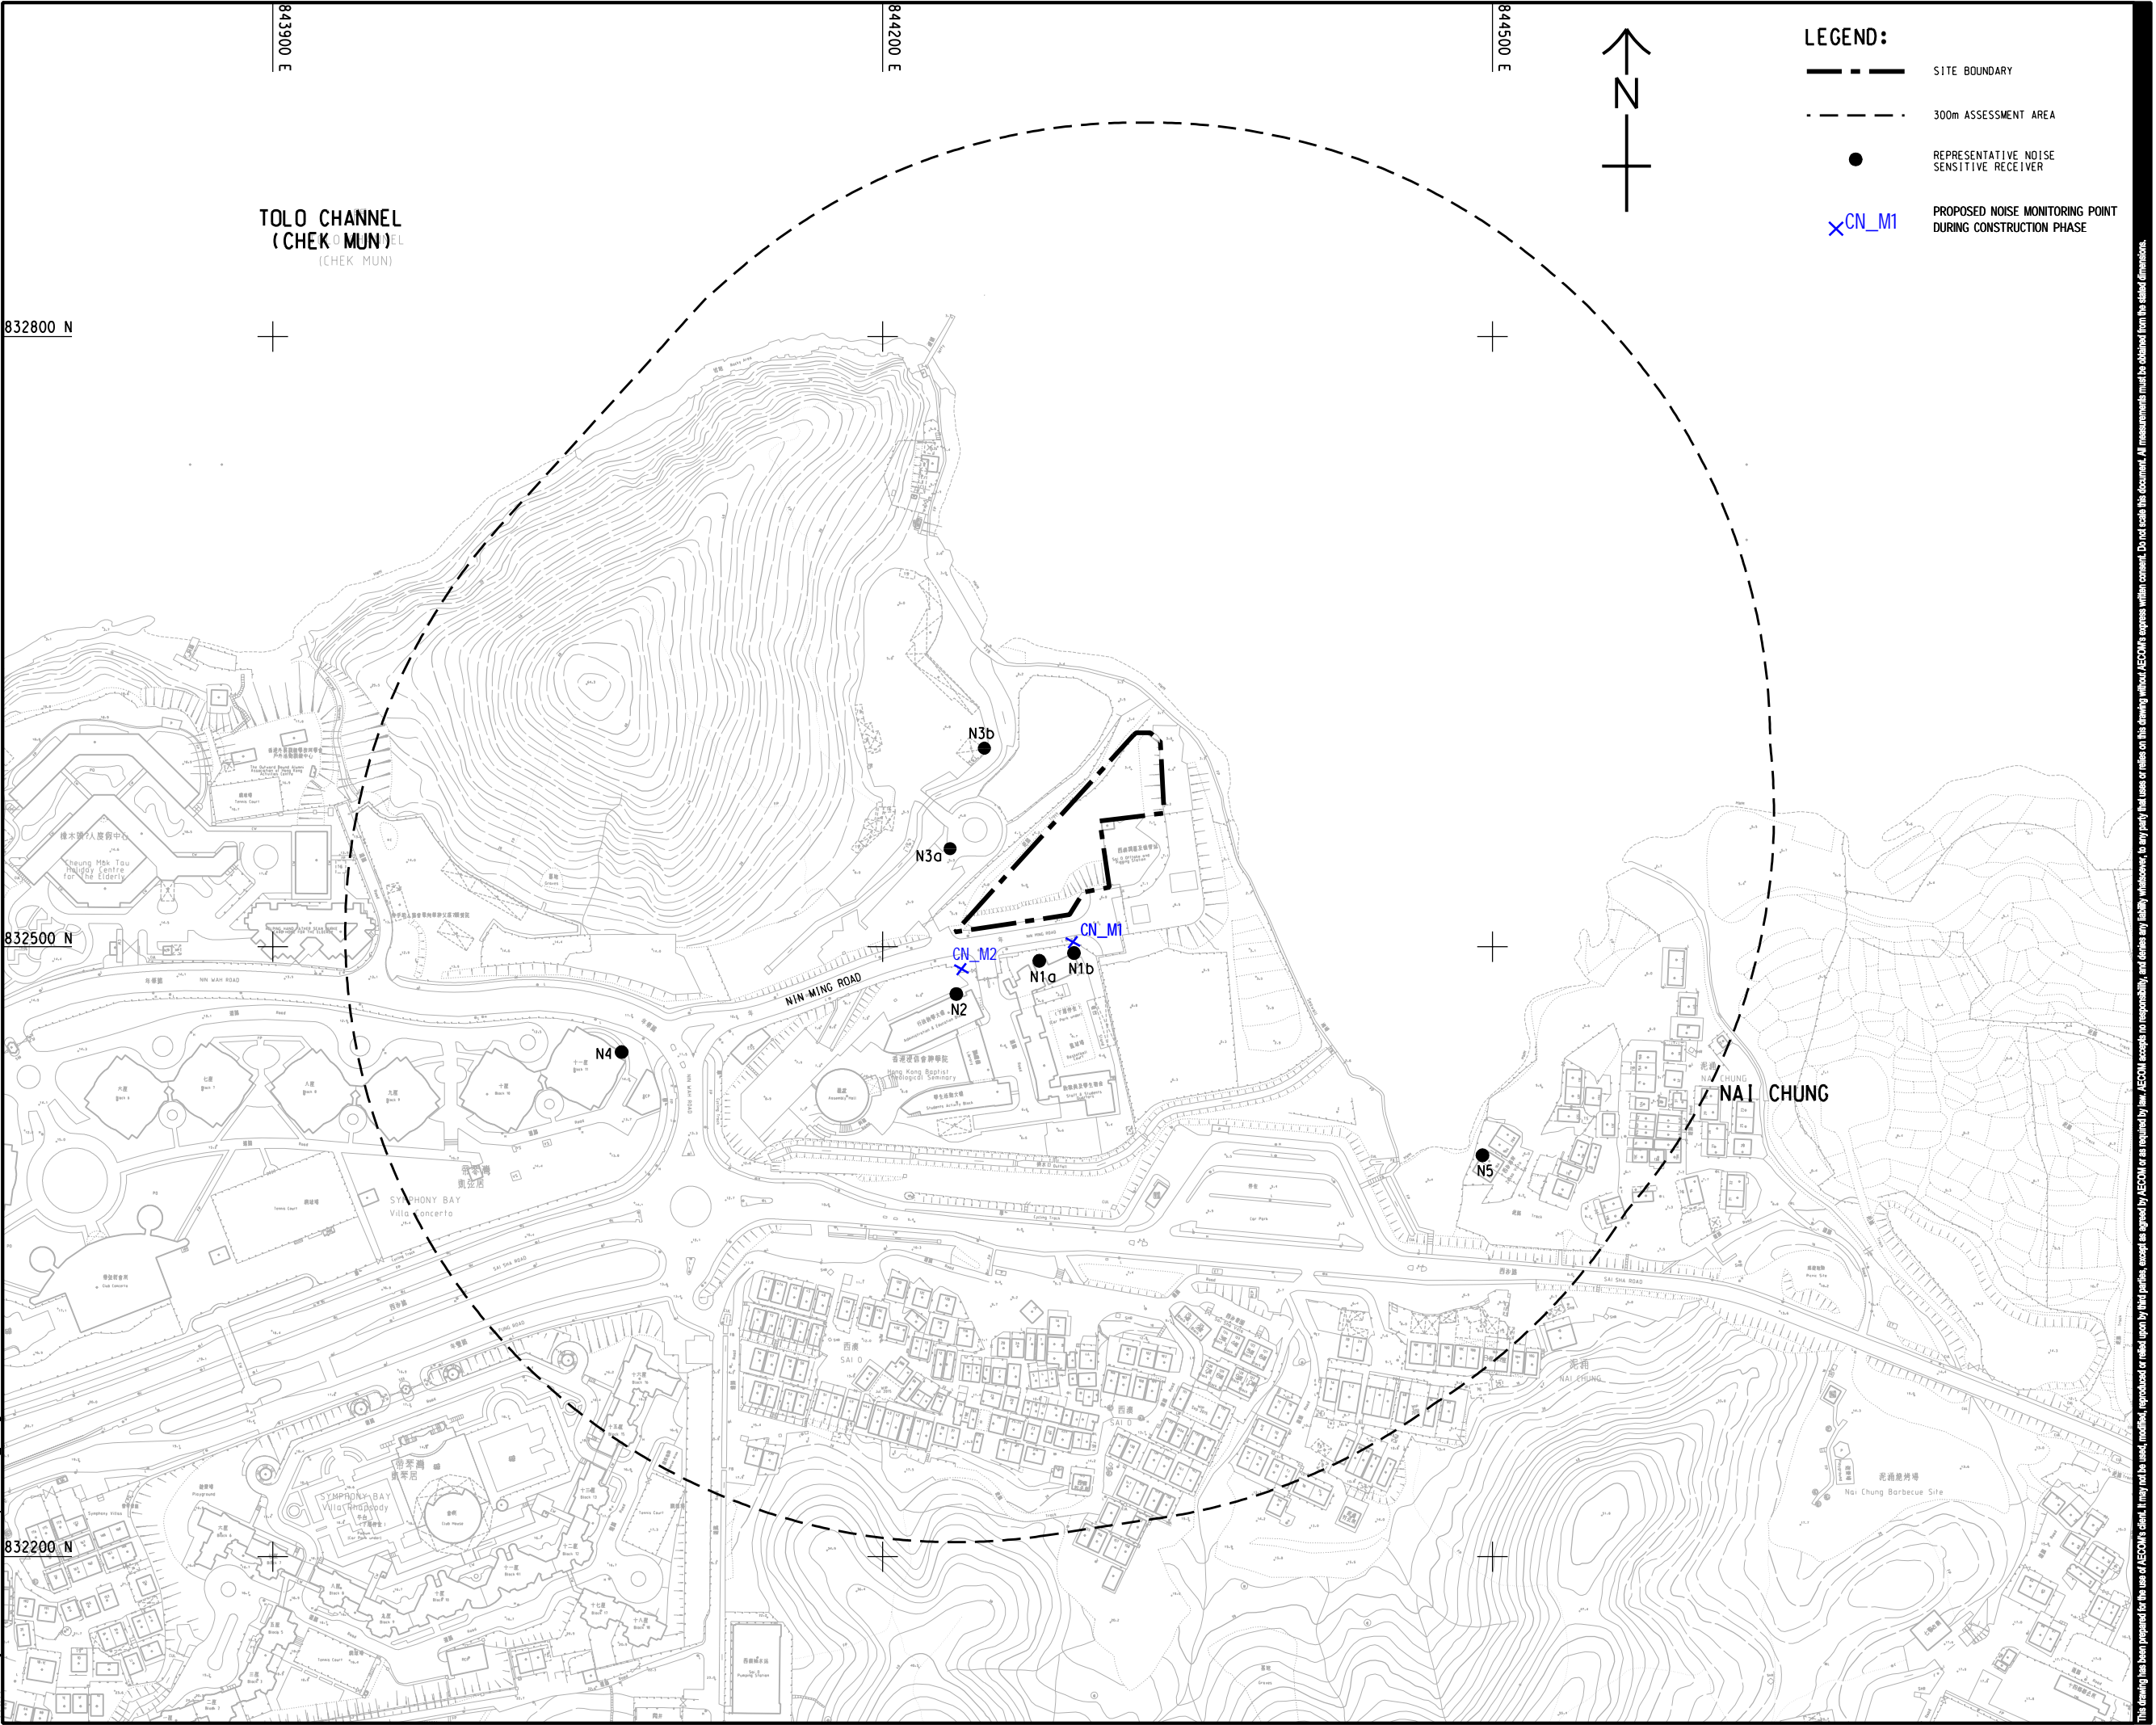

LEGEND:

- SITE BOUNDARY
- - - 300m ASSESSMENT AREA
- REPRESENTATIVE NOISE SENSITIVE RECEIVER
- ✕CN\_M1 PROPOSED NOISE MONITORING POINT DURING CONSTRUCTION PHASE

**AECOM**

**PROJECT**  
項目

**TOLO HARBOUR  
SEWERAGE OF  
UNSEWERED AREAS  
STAGE 2 -  
INVESTIGATION, DESIGN  
AND CONSTRUCTION**

**CLIENT**  
業主

**渠務署  
Drainage Services Department**

**CONSULTANT**  
工程顧問公司

**AECOM Asia Company Ltd.  
www.aecom.com**

**SUB-CONSULTANTS**  
分判工程顧問公司

| ISSUE/REVISION<br>修訂 |            |                        |            |
|----------------------|------------|------------------------|------------|
|                      |            |                        |            |
|                      |            |                        |            |
|                      |            |                        |            |
|                      |            |                        |            |
|                      |            |                        |            |
| I/R<br>修訂            | DATE<br>日期 | DESCRIPTION<br>內容摘要    | CHK.<br>校核 |
| STATUS<br>階段         |            |                        |            |
| SCALE<br>比例          |            | DIMENSION UNIT<br>尺寸單位 |            |
| A1 1 : 1500          |            | METRES                 |            |
| KEY PLAN<br>索引圖      |            |                        |            |

**PROJECT NO.**  
項目編號

**60547289**

**CONTRACT NO.**  
合約編號

**SHEET TITLE**  
圖紙名稱

**LOCATIONS OF PROPOSED NOISE  
MONITORING POINT**

**SHEET NUMBER**  
圖紙編號


**60547289/EM&A/FIGURE 3.1**

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, for any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the related dimensions.

# Appendix A

---

## Project Organization Chart

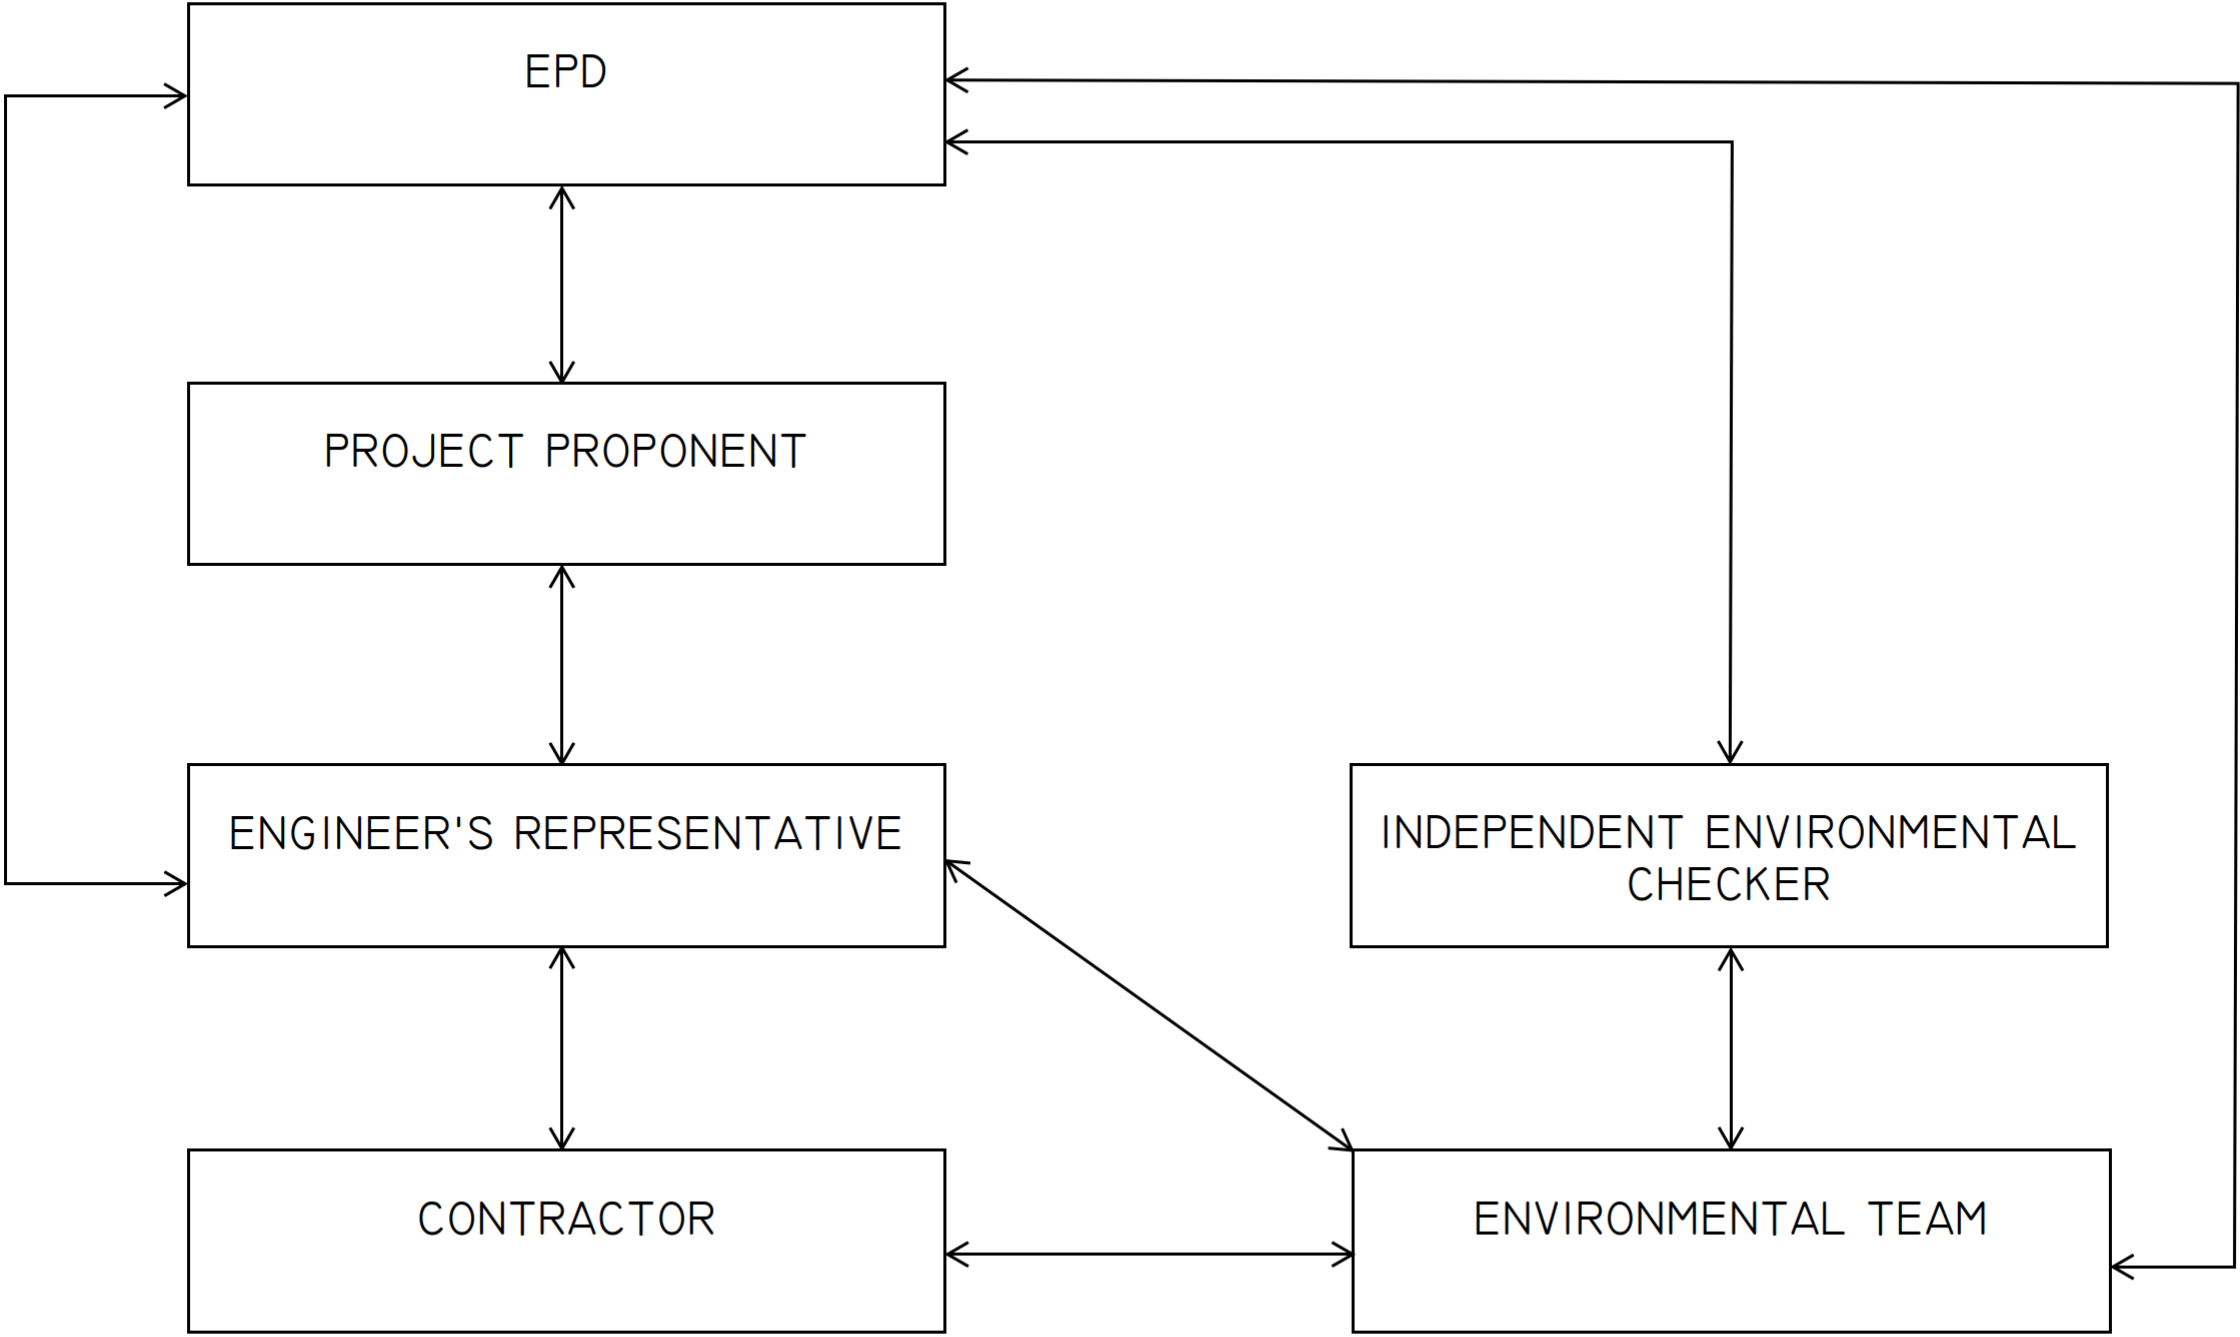

LEGEND:


↔ LINE OF COMMUNICATION

**AECOM**

PROJECT  
项目

TOLO HARBOUR  
SEWERAGE OF  
UNSEWERED AREAS  
STAGE 2 -  
INVESTIGATION, DESIGN  
AND CONSTRUCTION

CLIENT  
業主



渠務署  
Drainage Services Department

CONSULTANT  
工程顧問公司

AECOM Asia Company Ltd.  
www.aecom.com

SUB-CONSULTANTS  
分判工程顧問公司

ISSUE/REVISION  
修訂

|           |            |                     |            |
|-----------|------------|---------------------|------------|
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
|           |            |                     |            |
| I/R<br>修訂 | DATE<br>日期 | DESCRIPTION<br>內容摘要 | CHK.<br>校核 |

STATUS  
階段

SCALE  
比例

A1 1 : AS SHOWN

DIMENSION UNIT  
尺寸單位

METRES

KEY PLAN  
索引圖

PROJECT NO.  
項目編號

60547289

CONTRACT NO.  
合約編號

SHEET TITLE  
圖紙名稱

PROJECT ORGANISATION

SHEET NUMBER  
圖紙編號

60547289/EM&A/FIGURE 1.2

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

# Appendix B

---

## Construction Programme

| ID  | Activity  | Days   | Start | Finish      | 2024        |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|---|-----------|--|-------|-------------|-------------|----|----|----|----|--|----|----|-------|----|----|----|----|----|----|--|-----|----|----|----|----|------|
|   |           |  |       |             | March       |    |    |    |    |  |    |    | April |    |    |    |    |    |    |  | May |    |    |    |    |      |
|   |           |  |       |             |             | 03 | 10 | 17 | 24 |  | 31 | 07 | 14    | 21 | 28 | 05 | 12 | 19 | 26 |  | 02  | 09 | 16 | 23 | 30 | July |
|   | TLR3140   | Zone 1: Diversion to Permanent Road                                  | 6     | 17-May-24   | 23-May-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TLR3150   | Zone 1: Remove Temp. Road and Reinstate Area                         | 24    | 24-May-24   | 21-Jun-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TLR3210   | Zone 2: Drainage, 50m  | 52    | 02-Apr-24   | 04-Jun-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TLR3225   | Zone 2: gasmain and telecom duct                                     | 24    | 05-Jun-24   | 04-Jul-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Tseng Tau Road (Section 2 of the Works)     |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Area 7.2 - Tseng Tau Road (R400: Ch100-250) |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| West bound                                  |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTR1550   | Drainage and surface channel behind RW6 and RW27-29                  | 96    | 31-Oct-23 A | 30-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Utilities Works                             |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTR1570   | CLP (2 x 150m), 50m/wk   | 26    | 09-Oct-23 A | 30-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTR2710   | CMHK-60m,HGC-150m,HKBN-150m,HKT-230m,SMT-150m,TGT-30m,VTL-150m       | 26    | 16-Oct-23 A | 08-May-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Soft Landscaping Works                      |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTR3010   | Soft Lanscaping Works  | 18    | 01-Mar-24 A | 31-May-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Tseng Tau Pumping Station                   |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| External Works and ABWF/E&M Works           |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1120 | E&M works  | 140   | 21-Nov-22 A | 22-Mar-24 A |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1130 | ABWF works (interior finish and building envelope)                   | 100   | 25-Aug-22 A | 22-Mar-24 A |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1135 | External works (fencing, planter, EVA, signage, etc)                 | 26    | 03-May-23 A | 22-Mar-24 A |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| T&C and Statutory Inspection                |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1140 | T&C  | 23    | 25-Sep-23 A | 11-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1150 | FSD Inspection, ASD Inspection, OP (aftrer power on in mid Nov 2023) | 24    | 02-Apr-24*  | 30-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | TTSPS1160 | Completion of Section 2  | 0     |             | 30-Apr-24*  |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| Sai O Pumping Station (Section 4)           |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| ABWF Works                                  |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS5010  | Interior finish - pump room  | 52    | 25-Aug-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS5020  | Exterior finish  | 52    | 04-Sep-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS5030  | Roof finish  | 52    | 29-Sep-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS5040  | External works   | 40    | 07-Oct-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
| E&M Works and OP                            |           |  |       |             |             |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6020  | E&M works - pump room below ground                                   | 71    | 09-Oct-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6030  | E&M works - pump room above ground                                   | 82    | 09-Oct-23 A | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6040  | E&M works - external   | 16    | 02-Apr-24   | 20-Apr-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6050  | FS inspection  | 58    | 15-Apr-24   | 24-Jun-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6060  | Testing and Commissioning  | 49    | 02-Apr-24   | 31-May-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |
|   | SOPS6070  | OP inspection  | 6     | 18-Jun-24   | 24-Jun-24   |    |    |    |    |  |    |    |       |    |    |    |    |    |    |  |     |    |    |    |    |      |

# Appendix C

---

## Equipment Calibration Certificates



## Air Quality Monitoring Equipment

**TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET**

|                |               |                        |           |
|----------------|---------------|------------------------|-----------|
| Model:         | Tisch TE-5170 | Date of Calibration:   | 23-Feb-24 |
| Equipment No.: | HVS-05        | Next Calibration Date: | 22-Apr-24 |
| Location:      |               | Technician:            | Yin Ho    |

| CONDITIONS                |         |                             |     |
|---------------------------|---------|-----------------------------|-----|
| Sea Level Pressure (hPa): | 1019.90 | Corrected Pressure (mm Hg): | 765 |
| Temperature (°C):         | 20.4    | Temperature (K):            | 293 |

| CALIBRATION ORIFICE |                |                 |          |
|---------------------|----------------|-----------------|----------|
| Model:              | Tisch TE-5025A | Qstd Slope:     | 2.08482  |
| Serial No.:         | 2456           | Qstd Intercept: | -0.02977 |
| Calibration Date:   | 1-Jun-23       | Expiry Date:    | 1-Jun-24 |

| CALIBRATIONS |              |              |          |                            |           |                |  |
|--------------|--------------|--------------|----------|----------------------------|-----------|----------------|--|
| Plate No.    | H2O (L) (in) | H2O (R) (in) | H2O (in) | Qstd (m <sup>3</sup> /min) | I (chart) | IC (corrected) | LINEAR REGRESSION  |
| 18           | 5.80         | -6.40        | 12.200   | 1.708                      | 58.00     | 58.64          | Slope = 24.0830<br>Intercept = 17.3042<br>Corr. coeff.= 0.9969 |
| 13           | 4.80         | -4.60        | 9.400    | 1.501                      | 52.00     | 52.58          |  |
| 10           | 3.60         | -3.40        | 7.000    | 1.297                      | 49.00     | 49.54          |  |
| 7            | 2.20         | -2.40        | 4.600    | 1.054                      | 42.00     | 42.47          |  |
| 5            | 1.00         | -1.60        | 2.600    | 0.796                      | 36.00     | 36.40          |  |

**Calculations:**


Qstd = 1/m[Sqrt(H2O(Pa/Pstd)(Tstd/Ta))-b]  
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate  
IC = corrected chart response  
I = actual chart response  
m = calibrator Qstd slope  
b = calibrator Qstd intercept  
Ta = actual temperature during calibration (deg K)  
Pa = actual pressure during calibration (mm Hg)  
Tstd = 298 deg K  
Pstd = 760 mm Hg

**For subsequent calculation of sampler flow:**  
 $1/m((I)[\text{Sqrt}(298/\text{Tav})(\text{Pav}/760)]-b)$

m = sampler slope  
b = sampler intercept  
I = chart response  
Tav = daily average temperature  
Pav = daily average pressure

**FLOW RATE CHART**

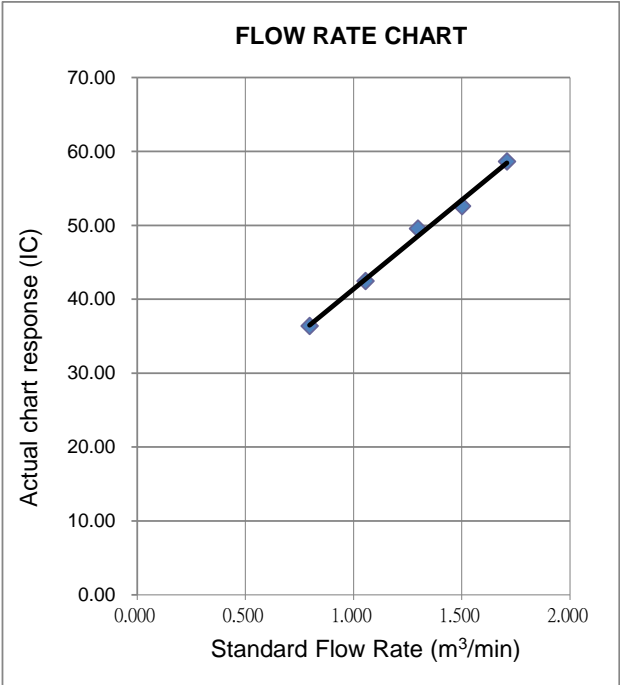

Calibrated by : Ho Chun Yiu Date : 23 Feb 2024 Supervised by : [Signature]

Date : 26 Feb 2024

# Certificate of Calibration

**Calibration Certification Information**

**Cal. Date:** June 1, 2023      **Rootsmeter S/N:** 438320      **Ta:** 295 °K  
**Operator:** Jim Tisch      **Pa:** 751.8 mm Hg  
**Calibration Model #:** TE-5025A      **Calibrator S/N:** 2456

| Run | Vol. Init (m3) | Vol. Final (m3) | ΔVol. (m3) | ΔTime (min) | ΔP (mm Hg) | ΔH (in H2O) |
|-----|----------------|-----------------|------------|-------------|------------|-------------|
| 1   | 1              | 2               | 1          | 1.4360      | 3.2        | 2.00        |
| 2   | 3              | 4               | 1          | 1.0210      | 6.4        | 4.00        |
| 3   | 5              | 6               | 1          | 0.9080      | 8.0        | 5.00        |
| 4   | 7              | 8               | 1          | 0.8670      | 8.8        | 5.50        |
| 5   | 9              | 10              | 1          | 0.7170      | 12.8       | 8.00        |

**Data Tabulation**

| Vstd (m3)   | Qstd (x-axis) | $\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis) | Va        | Qa (x-axis) | $\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis) |
|-------------|---------------|--|-----------|-------------|---|
| 0.9951      | 0.6929        | 1.4137   | 0.9957    | 0.6934      | 0.8859  |
| 0.9908      | 0.9704        | 1.9993   | 0.9915    | 0.9711      | 1.2528  |
| 0.9887      | 1.0889        | 2.2353   | 0.9894    | 1.0896      | 1.4007  |
| 0.9876      | 1.1391        | 2.3444   | 0.9883    | 1.1399      | 1.4690  |
| 0.9823      | 1.3700        | 2.8275   | 0.9830    | 1.3710      | 1.7717  |
| <b>QSTD</b> | <b>m=</b>     | <b>2.08482</b>   | <b>QA</b> | <b>m=</b>   | <b>1.30548</b>  |
|             | <b>b=</b>     | <b>-0.02977</b>  |           | <b>b=</b>   | <b>-0.01866</b>   |
|             | <b>r=</b>     | <b>0.99997</b>   |           | <b>r=</b>   | <b>0.99997</b>  |

**Calculations**

|  |   |   |                                |
|--|---|---|--------------------------------|
| <b>Vstd=</b>   | $\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$ | <b>Va=</b>  | $\Delta Vol((Pa-\Delta P)/Pa)$ |
| <b>Qstd=</b>   | $Vstd/\Delta Time$                        | <b>Qa=</b>  | $Va/\Delta Time$               |
| <b>For subsequent flow rate calculations:</b>  |   |   |                                |
| <b>Qstd=</b> $1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$ |   | <b>Qa=</b> $1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$ |                                |

**Standard Conditions**
**Tstd:** 298.15 °K

**Pstd:** 760 mm Hg

**Key**

ΔH: calibrator manometer reading (in H2O)

ΔP: rootsmeter manometer reading (mm Hg)

Ta: actual absolute temperature (°K)

Pa: actual barometric pressure (mm Hg)

b: intercept

m: slope

**RECALIBRATION**

US EPA recommends annual recalibration per 1998  
 40 Code of Federal Regulations Part 50 to 51,  
 Appendix B to Part 50, Reference Method for the  
 Determination of Suspended Particulate Matter in  
 the Atmosphere, 9.2.17, page 30

## CALIBRATION REPORT OF WIND METER


|  |  |                        |             |
|--|--|------------------------|-------------|
| EP No.: EP-597/2021                                |  | Date of Calibration:   | 26-Feb-2024 |
| Location: Sai O Trunk Sewer Sewage Pumping Station |  | Next Calibration Date: | 25-Aug-2024 |
|  |  | Technician:            | Yin Ho      |
| Brand:   | Global Water   |                        |             |
| Model:   | GL500-7-2  | Equipment ID:          | WS-03       |
| Anemometer   |  |                        |             |
| Brand:   | Smart Sensor   |                        |             |
| Model:   | AR816  | Equipment ID:          | AM-001      |
| Procedures:  |  |                        |             |
| 1. Wind Still Test:                                | The wind speed sensor was held by hand until stabilized.                                       |                        |             |
| 2. Wind Speed Test:                                | By direct comparison the reading between the wind speed sensor and the Anemometer.             |                        |             |
| 3. Wind Direction Test:                            | The wind meter was calibrated in-situ and compared with a marine compass from four directions. |                        |             |

### Wind Still Test:

| Wind Speed (m/s) |
|------------------|
| 0.00             |

### Wind Speed Test:

| Global Water (m/s) | Anemometer (m/s) |
|--------------------|------------------|
| 1.0                | 1.0              |
| 2.3                | 2.5              |
| 4.2                | 4.1              |

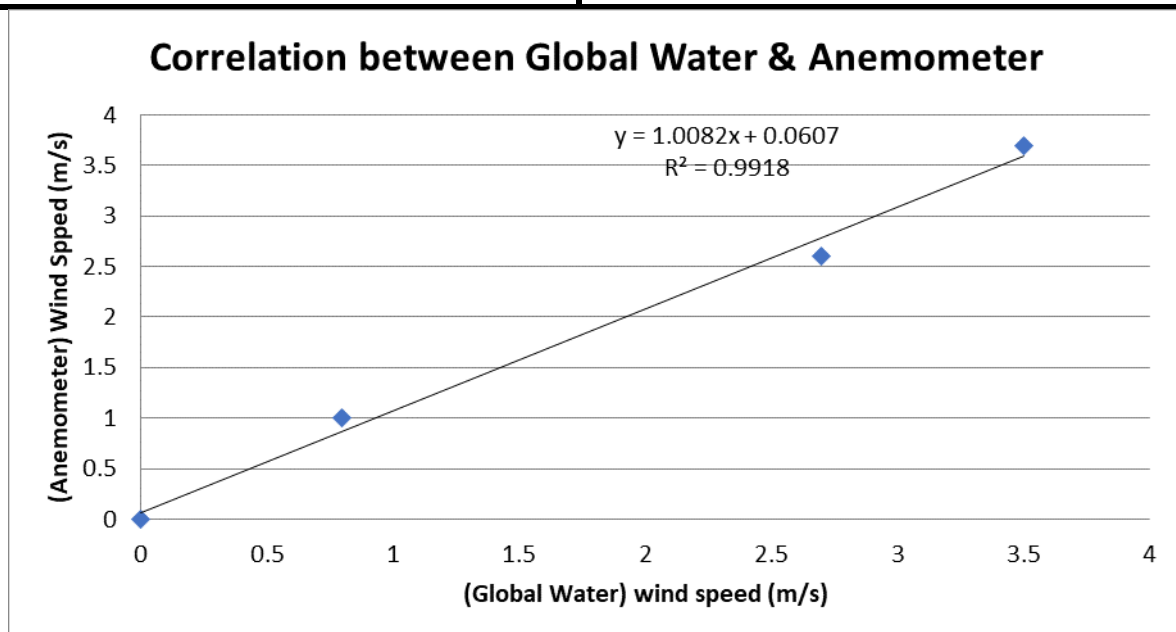

### Remarks:

- Actual Wind Speed Value (m/s) =  $1.0082 \times (\text{Reading of Global Water Instrument}) + 0.0607$
- Correlation coefficient ( $R^2$ ) = 0.9918
- Acceptable Range:  $R^2 \geq 0.99$



## FUGRO TECHNICAL SERVICES LIMITED

Room 723 & 725, 7/F, Block B,  
Profit Industrial Building,  
1-15 Kwai Fung Crescent, Kwai Fong,  
Hong Kong.

### CALIBRATION REPORT OF WIND METER

Wind Direction Test:

|     | Marine Compass (o) |
|-----|--------------------|
| 2   | 0                  |
| 46  | 45                 |
| 92  | 90                 |
| 271 | 270                |

**Toby Wan**  
Project Consultant

**Report Date:** 26/02/2023

Report No. : 212769CA233072

Page 1 of 1

**CALIBRATION CERTIFICATE OF ANEMOMETER****Client Supplied Information**

Client : Fugro Technical Services Ltd.

Project : Calibration Services

**Details of Unit Under Test, UUT**

Description : Anemometer

Manufacturer : Smart Sensor

Model No. : AR816

Serial No. : NA

Equipment ID.: AM-001

Next Calibration Date : 23-Apr-2024

**Laboratory Information**

Details of Reference Equipment –

Description : Reference Anemometer

Equipment ID.: R-101-4

Date of Calibration : 24-Apr-2023 Ambient Temperature : 22 °C

Calibration Location : Calibration Laboratory of FTS

Method Used : In-house method R-C-279

**Calibration Results :**

| Reference Reading<br>(m/s) | UUT Reading<br>(m/s) | Error<br>(m/s) |
|----------------------------|----------------------|----------------|
| 2.00                       | 2.0                  | 0.0            |
| 4.00                       | 4.0                  | 0.0            |
| 6.00                       | 6.0                  | 0.0            |
| 8.00                       | 8.2                  | 0.2            |
| 10.02                      | 10.3                 | 0.3            |

**Remark :**

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The reported readings in this calibration are an average from 10 trials.

Checked by :  Date : 27-4-2023 Certified by : KT Leung Date : 27-4-2023  
CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

**\*\* End of Report \*\***

## Noise Monitoring Equipment



## **CALIBRATION CERTIFICATE OF SOUND LEVEL METER**

### **Client Supplied Information**

Client : Materialab Consultants Ltd.

Project : Calibration Services

### **Details of Unit Under Test, UUT -**

Description : Sound Level Meter  
Manufacturer : Casella

|            | Meter   | Microphone | Preamplifier |
|------------|---------|------------|--------------|
| Model No.  | CEL-63X | CE-251     | CEL-495      |
| Serial No. | 1488300 | 04727      | 005347       |

Equipment ID : N/A  
Next Calibration Date : 14-Jul-2024  
Specification Limit : EN 61672-1: 2003 Class 1

### **Laboratory Information**

#### **Details of Reference Equipment -**

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)  
Equipment ID. : R-108-1  
Date of Receipt : 13-Jul-2023  
Date of Calibration : 15-Jul-2023  
Calibration Location : Calibration Laboratory of FTS  
Method Used : By direct comparison

Ambient Temperature : 20±2 °C  
Relative Humidity : <80% R.H.

### **Calibration Results :**

| Parameters                     |             | Mean Value (dB) | Specification Limit(dB) |
|--------------------------------|-------------|-----------------|-------------------------|
| A-weighting frequency response | 4000Hz      | 1.3             | 2.6 to -0.6             |
|                                | 2000Hz      | 1.3             | 2.8 to -0.4             |
|                                | 1000Hz      | 0.0             | 1.1 to -1.1             |
|                                | 500Hz       | -3.3            | -1.8 to -4.6            |
|                                | 250Hz       | -8.8            | -7.2 to -10.0           |
|                                | 125Hz       | -16.2           | -14.6 to -17.6          |
|                                | 63Hz        | -26.2           | -24.7 to -27.7          |
| Differential level linearity   | 94dB-104dB  | 0.0             | ± 0.6                   |
|                                | 104dB-114dB | 0.0             | ± 0.6                   |

### **Remarks :**

- The equipment used in this calibration is traceable to recognized National Standards.
- For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast
- The mean value is the average of four measurements.
- The equipment does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
- The values given in this Calibration Certificate only relate to the values at the time of the test and any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

Checked by :  Date : 21-7-2023 Certified by :  Date : 27-7-2023  
CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

\*\* End of Report \*\*



Report no.: 212769CA233276(1)

Page 1 of 1

**CALIBRATION CERTIFICATE OF SOUND CALIBRATOR**

Client : Materialab Consultants Ltd.

Project : Calibration Services

**Client Supplied Information**

Details of Unit Under Test, UUT -

Description : Sound Calibrator  
Manufacturer : Casella (Model CEL-120/1)  
Serial No. : 5230758  
Equipment ID : N/A

Next Calibration Date : 14-Jul-2024

Specification Limit : EN 60942: 2003 Class 1

**Laboratory Information**

Details of Calibration Equipment -

Description : Reference Sound level meter  
Equipment ID. : R-119-2

Date of Receipt : 13-Jul-2023

Date of Calibration : 15-Jul-2023

Calibration Location : Calibration Laboratory of FTS Ambient Temperature :  $20 \pm 2$  °C

Method Used : By direct comparison Relative Humidity : &lt; 80 %RH

**Calibration Results :**

| Parameters (Setting of UUT) | Mean Value (error of measurement) | Specification Limit(dB) |
|-----------------------------|-----------------------------------|-------------------------|
| 94dB                        | -0.1 dB                           | ±0.4dB                  |
| 114dB                       | -0.1 dB                           |                         |

**Remarks :**

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The unit under test complies with the specification limit.
4. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties quoted will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

Checked by :  Date : 21-7-2023 Certified by :  Date : 27-7-2023  
CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

\*\* End of Report \*\*

# Appendix D

---

## Environmental Monitoring Schedule

**Project: EP-597/2021 Sai O Trunk Sewer Sewage Pumping Station**  
**Impact Air Quality & Noise Monitoring Schedule (March 2024)**

| Sun | Mon                     | Tue                 | Wed                 | Thur                | Fri                | Sat        |
|-----|-------------------------|---------------------|---------------------|---------------------|--------------------|------------|
|     |                         |                     |                     |                     | 1                  | 2<br>• AQM |
| 3   | 4<br>• Site Inspection  | 5                   | 6                   | 7                   | 8<br>• AQM<br>• NM | 9          |
| 10  | 11<br>• Site Inspection | 12                  | 13                  | 14<br>• AQM<br>• NM | 15<br>•            | 16         |
| 17  | 18<br>• Site Inspection | 19                  | 20<br>• AQM<br>• NM | 21                  | 22                 | 23         |
| 24  | 25<br>• Site Inspection | 26<br>• AQM<br>• NM | 27                  | 28<br>• AQM         | 29                 | 30         |
| 31  |                         |                     |                     |                     |                    |            |

**Remarks**

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition;
- Air Quality Monitoring(AQM): 3 x 1-hours TSP Monitoring in every 6 days;  
Monitoring Locations: CA\_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters
- Noise Monitoring(NM): one set of Leq (30 min) between 0700 and 1900 hours on normal weekdays once a week;  
Monitoring Locations: CN\_M1 In front of the HKBTS Staff & Students Quarters  
Monitoring Locations: CN\_M2 In front of the HKBTS Administration and Education Block
- Site Inspection: Once a week

**Project: EP-597/2021 Sai O Trunk Sewer Sewage Pumping Station**  
**Impact Air Quality & Noise Monitoring Schedule (April 2024)**

| Sun | Mon                                      | Tue                    | Wed                | Thur | Fri                 | Sat                 |
|-----|--|------------------------|--------------------|------|---------------------|---------------------|
|     | 1  | 2<br>• Site Inspection | 3<br>• AQM<br>• NM | 4    | 5                   | 6                   |
| 7   | 8<br>• Site Inspection                   | 9<br>• AQM<br>• NM     | 10                 | 11   | 12                  | 13                  |
| 14  | 15<br>• Site Inspection<br>• AQM<br>• NM | 16                     | 17                 | 18   | 19                  | 20<br>• AQM<br>• NM |
| 21  | 22<br>• Site Inspection                  | 23                     | 24                 | 25   | 26<br>• AQM<br>• NM | 27                  |
| 28  | 29<br>• Site Inspection                  | 30                     |                    |      |                     |                     |
| 31  |  |                        |                    |      |                     |                     |

**Remarks**

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition;
- Air Quality Monitoring(AQM): 3 x 1-hours TSP Monitoring in every 6 days;  
Monitoring Locations: CA\_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters
- Noise Monitoring(NM): one set of Leq (30 min) between 0700 and 1900 hours on normal weekdays once a week;  
Monitoring Locations: CN\_M1 In front of the HKBTS Staff & Students Quarters  
Monitoring Locations: CN\_M2 In front of the HKBTS Administration and Education Block
- Site Inspection: Once a week

# Appendix E

---

Air Quality & Construction Noise  
Monitoring Results

1-hr TSP Monitoring Results

Monitoring Location: CA\_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters

| Start Date | Start Time | Weather Condition | Filter Identification No. | Elapsed-Time Meter Reading |         | Sampling Time (min) | Temperature (K) | Atmospheric Pressure (mmHg) | Filter Paper Weight (g) |              |                    | Flow Rate (m³/min) |       |         | Total Volume (m³) | Concentration (µg/m³) |         |              |             |
|------------|------------|-------------------|---------------------------|----------------------------|---------|---------------------|-----------------|-----------------------------|-------------------------|--------------|--------------------|--------------------|-------|---------|-------------------|-----------------------|---------|--------------|-------------|
|            |            |                   |                           | Start                      | Stop    |                     |                 |                             | Initial Weight          | Final Weight | Particulate Weight | Intial             | Final | Average |                   | Value                 | Average | Action Level | Limit Level |
| 2-Mar-24   | 9:09       | Cloudy            | M13296                    | 6239.41                    | 6240.41 | 60                  | 285.0           | 766.7                       | 2.6978                  | 2.7107       | 0.013              | 1.33               | 1.24  | 1.29    | 77.15             | 167.2                 | 137.2   | 339          | 500         |
|            | 10:13      | Cloudy            | M13297                    | 6240.41                    | 6241.41 | 60                  | 285.0           | 766.7                       | 2.6860                  | 2.6963       | 0.010              | 1.24               | 1.24  | 1.24    | 74.59             | 138.1                 |         |              |             |
|            | 11:18      | Cloudy            | M13298                    | 6241.41                    | 6242.41 | 60                  | 285.0           | 766.7                       | 2.6826                  | 2.6904       | 0.008              | 1.20               | 1.24  | 1.22    | 73.31             | 106.4                 |         |              |             |
| 8-Mar-24   | 9:31       | Fine              | M13523                    | 6242.41                    | 6243.41 | 60                  | 291.8           | 764.2                       | 2.6940                  | 2.7022       | 0.008              | 1.30               | 1.26  | 1.28    | 76.81             | 106.8                 | 98.9    | 339          | 500         |
|            | 10:29      | Fine              | M13522                    | 6243.41                    | 6244.41 | 60                  | 291.8           | 764.2                       | 2.7108                  | 2.7167       | 0.006              | 1.30               | 1.30  | 1.30    | 78.07             | 75.6                  |         |              |             |
|            | 11:31      | Fine              | M13524                    | 6244.41                    | 6245.41 | 60                  | 291.8           | 764.2                       | 2.6935                  | 2.7020       | 0.009              | 1.22               | 1.26  | 1.24    | 74.28             | 114.4                 |         |              |             |
| 14-Mar-24  | 9:09       | Fine              | M13525                    | 6245.41                    | 6246.41 | 60                  | 292.8           | 763.0                       | 2.6736                  | 2.6817       | 0.008              | 1.21               | 1.25  | 1.23    | 74.00             | 109.5                 | 142.9   | 339          | 500         |
|            | 10:14      | Fine              | M13530                    | 6246.41                    | 6247.41 | 60                  | 292.8           | 763.0                       | 2.6841                  | 2.6947       | 0.011              | 1.21               | 1.21  | 1.21    | 72.74             | 145.7                 |         |              |             |
|            | 11:17      | Fine              | M13531                    | 6247.41                    | 6248.41 | 60                  | 292.8           | 763.0                       | 2.6898                  | 2.7022       | 0.012              | 1.17               | 1.21  | 1.19    | 71.48             | 173.5                 |         |              |             |
| 20-Mar-24  | 9:11       | Fine              | M12985                    | 6248.41                    | 6249.41 | 60                  | 293.8           | 766.9                       | 2.6628                  | 2.6868       | 0.024              | 1.26               | 1.30  | 1.28    | 76.61             | 313.3                 | 314.4   | 339          | 500         |
|            | 10:18      | Fine              | M12987                    | 6249.41                    | 6250.41 | 60                  | 293.8           | 766.9                       | 2.6771                  | 2.7074       | 0.030              | 1.51               | 1.51  | 1.51    | 90.47             | 334.9                 |         |              |             |
|            | 11:18      | Fine              | M12986                    | 6250.41                    | 6251.41 | 60                  | 293.8           | 766.9                       | 2.6633                  | 2.6900       | 0.027              | 1.51               | 1.51  | 1.51    | 90.47             | 295.1                 |         |              |             |
| 26-Mar-24  | 8:44       | Fine              | M12998                    | 6251.41                    | 6252.41 | 60                  | 299.2           | 762.8                       | 2.6416                  | 2.6564       | 0.015              | 1.27               | 1.23  | 1.25    | 75.21             | 196.8                 | 191.2   | 339          | 500         |
|            | 9:48       | Fine              | M12997                    | 6252.41                    | 6253.41 | 60                  | 299.2           | 762.8                       | 2.6403                  | 2.6550       | 0.015              | 1.03               | 1.03  | 1.03    | 61.51             | 239.0                 |         |              |             |
|            | 10:48      | Fine              | M12999                    | 6253.41                    | 6254.41 | 60                  | 299.2           | 762.8                       | 2.6490                  | 2.6592       | 0.010              | 1.23               | 1.23  | 1.23    | 73.96             | 137.9                 |         |              |             |
| 28-Mar-24  | 10:18      | Fine              | M13844                    | 6254.41                    | 6255.41 | 60.0                | 297.7           | 760.5                       | 2.7478                  | 2.7606       | 0.013              | 1.11               | 1.11  | 1.11    | 66.60             | 192.2                 | 191.8   | 339          | 500         |
|            | 11:20      | Fine              | M13843                    | 6255.41                    | 6256.41 | 60.0                | 297.7           | 760.5                       | 2.7220                  | 2.7355       | 0.014              | 1.11               | 1.03  | 1.07    | 64.11             | 210.6                 |         |              |             |
|            | 12:26      | Fine              | M13842                    | 6256.41                    | 6257.41 | 60.0                | 297.7           | 760.5                       | 2.7419                  | 2.7534       | 0.012              | 1.11               | 1.11  | 1.11    | 66.60             | 172.7                 |         |              |             |
|            |            |                   |                           |                            |         |                     |                 |                             |                         |              |                    |                    |       |         | Min               | 75.6                  |         |              |             |
|            |            |                   |                           |                            |         |                     |                 |                             |                         |              |                    |                    |       |         | Max               | 334.9                 |         |              |             |
|            |            |                   |                           |                            |         |                     |                 |                             |                         |              |                    |                    |       |         | Average           | 179.4                 |         |              |             |

Report No. : 215334EN241265



Page 1 of 1

### Test Report on Analysis of Filters

#### Information Supplied by Client

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

#### Laboratory Information

Filter paper I.D. : M13296, M13297, M13298

Date of receipt of sample : 04/03/2024


Date test completed : 05/03/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

#### Results :

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M13296            | 2.6978                   | 2.7107                 |
| M13297            | 2.6860                   | 2.6963                 |
| M13298            | 2.6826                   | 2.6904                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory : WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date : 18/04/2024  
\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 215334EN241265(1)



Page 1 of 1

### Test Report on Analysis of Filters

#### Information Supplied by Client

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

#### Laboratory Information

Filter paper I.D. : M13522, M13523, M13524

Date of receipt of sample : 11/03/2024


Date test completed : 12/03/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

#### Results :

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M13522            | 2.7108                   | 2.7167                 |
| M13523            | 2.6940                   | 2.7022                 |
| M13524            | 2.6935                   | 2.7020                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory: WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date : 18/04/2024

\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*



Report No. : 215334EN241265(2)



Page 1 of 1

### Test Report on Analysis of Filters

#### Information Supplied by Client

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

#### Laboratory Information

Filter paper I.D. : M13525, M13530, M13531

Date of receipt of sample : 15/03/2024


Date test completed : 18/03/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

#### Results :

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M13525            | 2.6736                   | 2.6817                 |
| M13530            | 2.6841                   | 2.6947                 |
| M13531            | 2.6898                   | 2.7022                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory : WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date :   
\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 215334EN241265(3)



Page 1 of 1

**Test Report on Analysis of Filters****Information Supplied by Client**

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

**Laboratory Information**

Filter paper I.D. : M12985, M12986, M12987

Date of receipt of sample : 20/03/2024

Date test completed : 27/03/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

**Results :**

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M12985            | 2.6628                   | 2.6868                 |
| M12986            | 2.6633                   | 2.6900                 |
| M12987            | 2.6771                   | 2.7074                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory : WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date : 18/04/2024

**\*\* End of Report \*\****Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 215334EN241265(4)



Page 1 of 1

### Test Report on Analysis of Filters

#### Information Supplied by Client

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

#### Laboratory Information

Filter paper I.D. : M12997, M12998, M12999

Date of receipt of sample : 26/03/2024


Date test completed : 27/03/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

#### Results :

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M12997            | 2.6403                   | 2.6550                 |
| M12998            | 2.6416                   | 2.6564                 |
| M12999            | 2.6490                   | 2.6592                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory : WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date :   
\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 215334EN241265(5)



Page 1 of 1

### Test Report on Analysis of Filters

#### Information Supplied by Client

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

#### Laboratory Information

Filter paper I.D. : M13842, M13843, M13844

Date of receipt of sample : 28/03/2024


Date test completed : 02/04/2024

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

#### Results :

| Filter paper I.D. | Initial wt. of filter, g | Final wt. of filter, g |
|-------------------|--------------------------|------------------------|
| M13842            | 2.7419                   | 2.7534                 |
| M13843            | 2.7220                   | 2.7355                 |
| M13844            | 2.7478                   | 2.7606                 |

Supervised by : C.H. Chiu

Certified by :   
Approved Signatory : WONG Kwok Fung, Raymond  
Manager – Chemistry Department

Date :   
\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

## Noise Monitoring Results

Monitoring Location : CN\_M1 In front of the HKBTS Staff & Students Quarters

| Date            | Weather | Wind Speed<br>(m/s) | Start Time | Noise Monitoring (30min) (dB(A))                                  |      |      |      |
|-----------------|---------|---------------------|------------|---|------|------|------|
|                 |         |                     |            | Corrected Leq   | Leq  | L90  | L10  |
| 8-Mar-24        | Fine    | 0.3                 | 8:57       | 59.8  | 56.8 | 53.0 | 64.0 |
| 14-Mar-24       | Fine    | 0.2                 | 9:17       | 64.3  | 61.3 | 56.5 | 63.0 |
| 20-Mar-24       | Fine    | 0.3                 | 9:18       | 65.1  | 62.1 | 58.0 | 64.0 |
| 26-Mar-24       | Fine    | 0.8                 | 9:17       | 57.8  | 54.8 | 51.5 | 56.0 |
| Average:        |         |                     |            | 62.7  |      |      |      |
| Baseline Level: |         |                     |            | 64.3  |      |      |      |
| Action Level:   |         |                     |            | When one valid documented complaint is received                   |      |      |      |
| Limit Level:    |         |                     |            | 70dB(A) for schools and 65dB(A) during school examination periods |      |      |      |

Monitoring Location : CN\_M2 In front of the HKBTS Administration and Education Block

| Date            | Weather | Wind Speed<br>(m/s) | Start Time | Noise Monitoring (30min) (dB(A))                                  |      |      |
|-----------------|---------|---------------------|------------|---|------|------|
|                 |         |                     |            | Leq   | L90  | L10  |
| 8-Mar-24        | Fine    | 0.9                 | 9:48       | 51.7  | 49.5 | 54.0 |
| 14-Mar-24       | Fine    | 0.1                 | 9:55       | 60.4  | 50.5 | 62.5 |
| 20-Mar-24       | Fine    | 0.3                 | 9:54       | 59.7  | 51.0 | 61.5 |
| 26-Mar-24       | Fine    | 0.8                 | 9:59       | 50.6  | 48.5 | 53.5 |
| Average:        |         |                     |            | 57.6  |      |      |
| Baseline Level: |         |                     |            | 62.5  |      |      |
| Action Level:   |         |                     |            | When one valid documented complaint is received                   |      |      |
| Limit Level:    |         |                     |            | 70dB(A) for schools and 65dB(A) during school examination periods |      |      |


Remarks: 1. Noise results at CN\_M1 were calculated by +3 dB (A) correction for free-field measurement.

# Appendix F



---

Air Quality & Construction Noise  
Monitoring Graphs

## 1-hr TSP Monitoring Graph

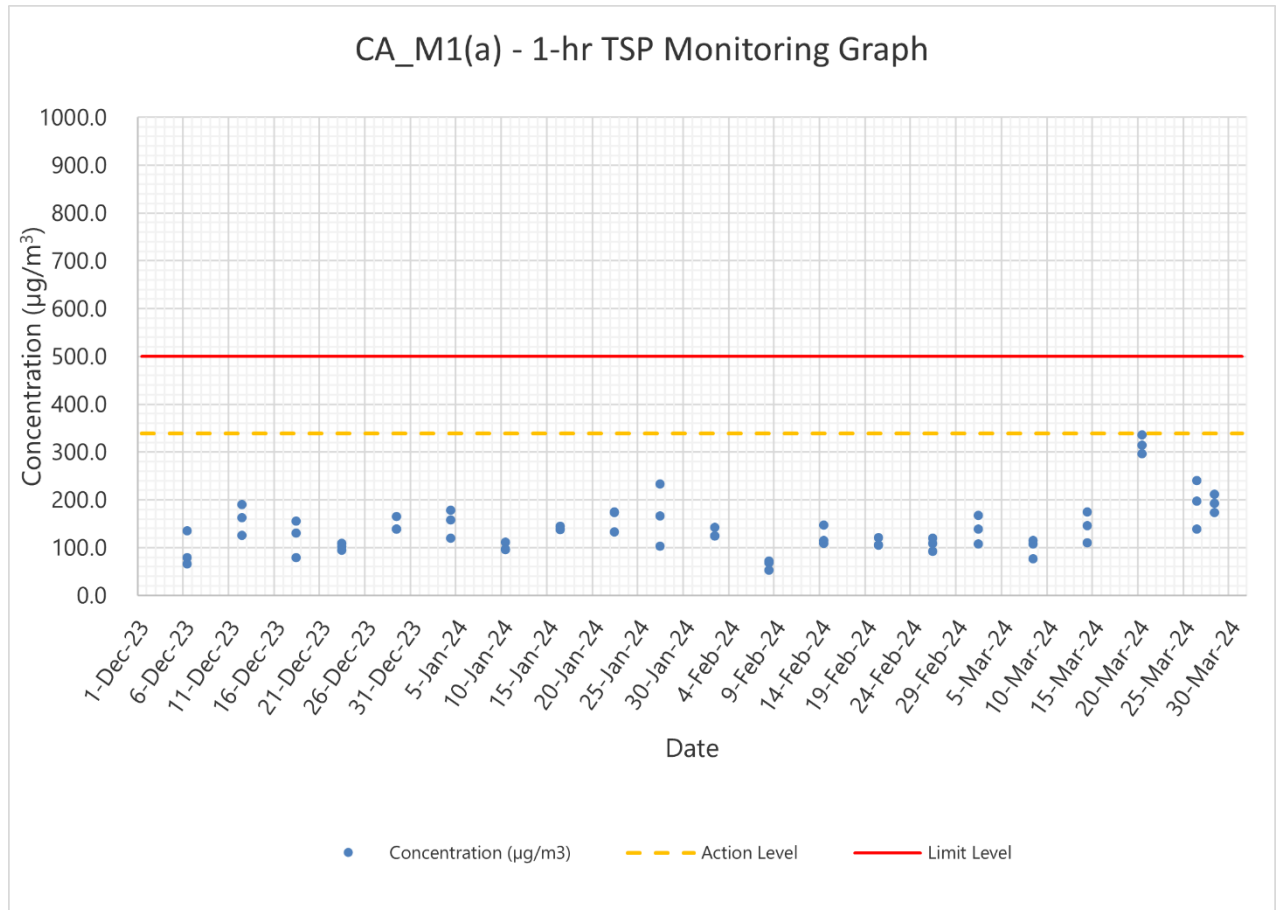

Noise Monitoring Graph

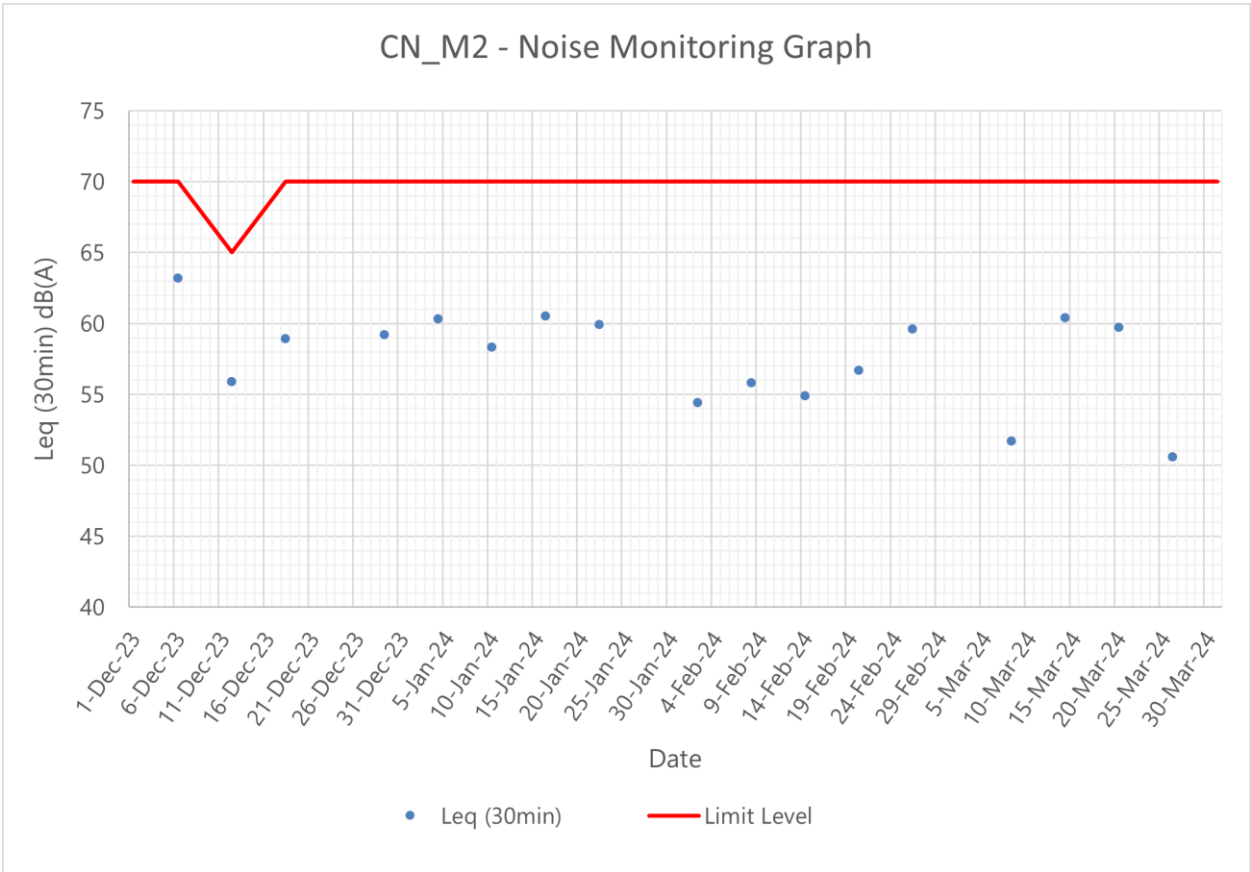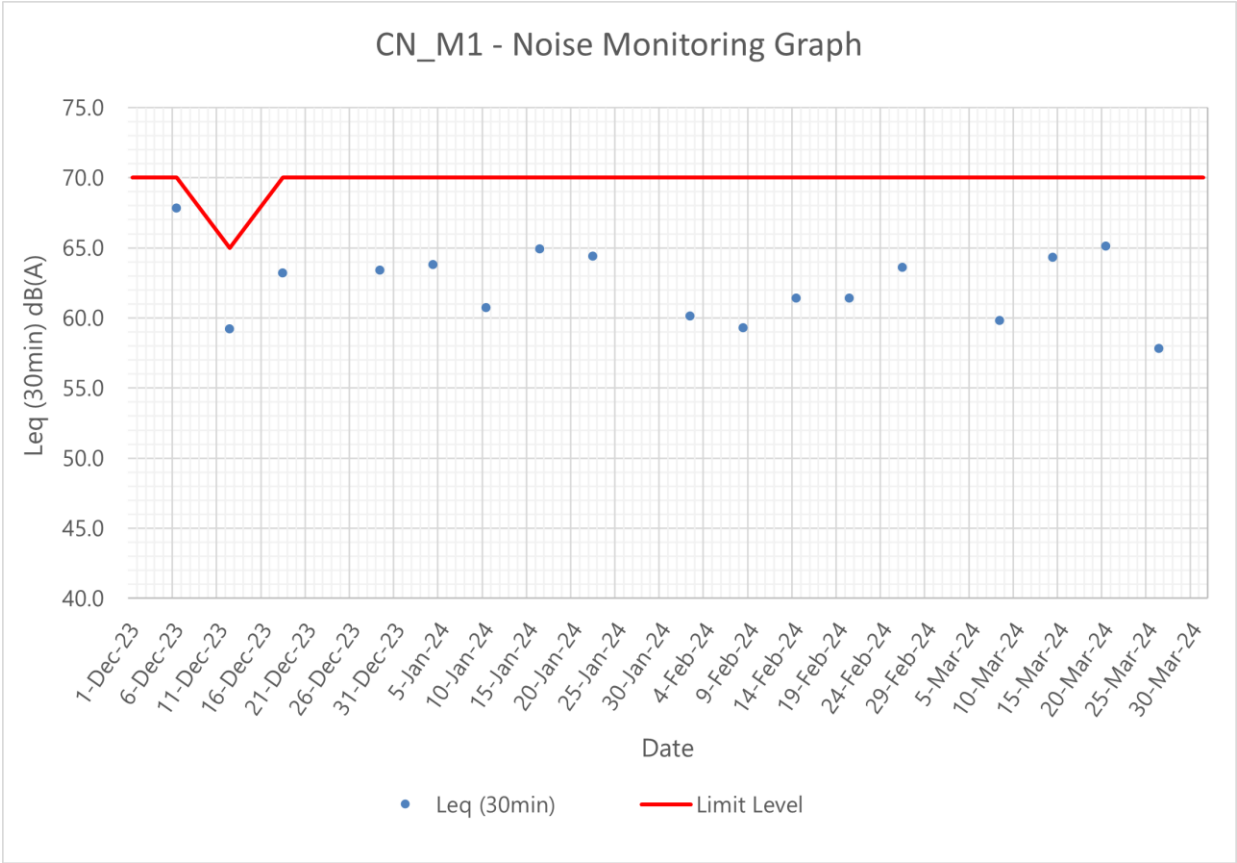



# Appendix G

---

Action and Limit Level

### Action and Limit Levels for Air Quality

| Monitoring Parameter | Monitoring Station | Action Level                 | Limit Level                  |
|----------------------|--------------------|------------------------------|------------------------------|
| 1-hour TSP           | CA_M1(a)           | 339 $\mu\text{g}/\text{m}^3$ | 500 $\mu\text{g}/\text{m}^3$ |

### Action and Limit Levels for Construction Noise

| Monitoring Parameter   | Monitoring Station | Action Level                                 | Limit Level  |
|--|--------------------|--|--|
| 0700-1900 hours in<br>normal weekdays<br>$\text{LA}_{\text{eq}}$ (30min) | CN_M1              | When one documented<br>complaint is received | 70dB(A) during normal teaching period &<br>65 dB(A) during examination periods |
|  | CN_M2              |  |  |

Remark:

CN\_M1: Free-field measurement (+3 dB(A) correction has been applied).

# Appendix H

---

## Event and Action Plan

## Event and Action Plan for Air Quality (Construction Dust)

| EVENT   | ACTION   |   |   |   |
|---|--|---|---|---|
|   | ET   | IEC   | ER  | Contractor  |
| Action level being exceeded by one sampling                     | <ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of complaint and propose remedial measures;</li> <li>2. Inform Contractor, IEC and ER;</li> <li>3. Repeat measurement to confirm finding; and</li> <li>4. Increase monitoring frequency to daily.</li> </ol>   | <ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method; and</li> <li>3. Review and advise the ET and ER on the effectiveness of the proposed remedial measures.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Notify Contractor.</li> </ol>   | <ol style="list-style-type: none"> <li>1. Identify source(s), investigate the causes of exceedance and propose remedial measures;</li> <li>2. Implement remedial measures; and</li> <li>3. Amend working methods agreed with the ER as appropriate.</li> </ol>  |
| Action level being exceeded by two or more consecutive sampling | <ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform Contractor, IEC and ER;</li> <li>3. Advise the Contractor and ER on the effectiveness of the proposed remedial measures;</li> <li>4. Repeat measurements to confirm findings;</li> <li>5. Increase monitoring frequency to daily;</li> <li>6. Discuss with IEC and Contractor on remedial actions required;</li> <li>7. If exceedance continues, arrange meeting with Contractor, IEC and ER; and</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>   | <ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET, ER and Contractor on possible remedial measures;</li> <li>4. Advise the ET and ER on the effectiveness of the proposed remedial measures; and</li> <li>5. Supervise Implementation of remedial measures.</li> </ol>          | <ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Submit proposals for remedial measures to the ER with a copy to ET and IEC within three working days of notification;</li> <li>3. Implement the agreed proposals; and</li> <li>4. Amend proposal as appropriate.</li> </ol>   |
| Limit level being exceeded by one sampling                      | <ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>2. Inform Contractor, IEC, ER, and EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily; and</li> <li>5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures; and</li> <li>5. Supervise implementation of remedial measures.</li> </ol>                     | <ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Identify source(s) and investigate the causes of exceedance;</li> <li>2. Take immediate action to avoid further exceedance;</li> <li>3. Submit proposals for remedial measures to ER with a copy to ET and IEC within three working days of notification;</li> <li>4. Implement the agreed proposals; and</li> <li>5. Amend proposal if appropriate.</li> </ol>   |
| Limit level being exceeded by two or more consecutive sampling  | <ol style="list-style-type: none"> <li>1. Notify IEC, ER, Contractor and EPD;</li> <li>2. Identify source;</li> <li>3. Repeat measurement to confirm findings;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol> | <ol style="list-style-type: none"> <li>1. Check monitoring data submitted by the ET;</li> <li>2. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>3. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and</li> <li>4. Supervise the implementation of remedial measures.</li> </ol> | <ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>3. Supervise the implementation of remedial measures; and</li> <li>4. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol> | <ol style="list-style-type: none"> <li>1. Identify source(s) and investigate the causes of exceedance;</li> <li>2. Take immediate action to avoid further exceedance;</li> <li>3. Submit proposals for remedial measures to the ER with a copy to the IEC and ET within three working days of notification;</li> <li>4. Implement the agreed proposals;</li> <li>5. Revise and resubmit proposals if problem still not under control; and</li> <li>6. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol> |

## Event and Action Plan for Noise (Construction Noise)

| EVENT        | ACTION   |   |  |   |
|--------------|--|---|--|---|
|              | ET   | IEC   | ER   | Contractor  |
| Action Level | <ol style="list-style-type: none"> <li>1. Notify IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures; and</li> <li>5. Increase monitoring frequency to check mitigation effectiveness.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Review the analyzed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; and</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>   | <ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem; and</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>  | <ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC; and</li> <li>2. Implement noise mitigation proposals.</li> </ol>  |
| Limit Level  | <ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC, ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol> | <ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and</li> <li>3. Supervise the implementation of remedial measures.</li> </ol> | <ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures properly implemented; and</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol> | <ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control; and</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol> |

# Appendix I

---

Weather and Meteorological

Conditions during Reporting Month

**Weather Condition (March 2024)**

| Date          | Mean Pressure (hPa) | Air Temperature |           |              | Mean Relative Humidity (%) | Total Rainfall (mm) |
|---------------|---------------------|-----------------|-----------|--------------|----------------------------|---------------------|
|               |                     | Maximum (°C)    | Mean (°C) | Minimum (°C) |                            |                     |
| 1 March 2024  | 1021.2              | 16.2            | 13.3      | 10.4         | 72                         | Trace               |
| 2 March 2024  | 1022.2              | 14.1            | 12.0      | 9.6          | 74                         | 0.3                 |
| 3 March 2024  | 1017.3              | 18.1            | 16.1      | 13.9         | 81                         | 0.2                 |
| 4 March 2024  | 1012.3              | 22.9            | 19.7      | 17.3         | 91                         | 1.4                 |
| 5 March 2024  | 1008.8              | 26.8            | 24.3      | 22.1         | 87                         | Trace               |
| 6 March 2024  | 1010.6              | 26.5            | 22.9      | 20.1         | 85                         | 0.1                 |
| 7 March 2024  | 1016.6              | 20.2            | 18.7      | 17.1         | 72                         | Trace               |
| 8 March 2024  | 1018.8              | 22.4            | 18.8      | 15.7         | 64                         | 0.2                 |
| 9 March 2024  | 1019.4              | 19.1            | 16.6      | 15.1         | 73                         | 2.1                 |
| 10 March 2024 | 1021.0              | 16.8            | 16.0      | 15.3         | 83                         | 4.6                 |
| 11 March 2024 | 1018.9              | 18.6            | 17.2      | 16.0         | 91                         | 11.7                |
| 12 March 2024 | 1018.8              | 24.0            | 19.3      | 15.6         | 61                         | 0.0                 |
| 13 March 2024 | 1018.6              | 21.2            | 19.4      | 17.7         | 66                         | Trace               |
| 14 March 2024 | 1017.3              | 22.0            | 19.8      | 18.6         | 71                         | 0.0                 |
| 15 March 2024 | 1017.2              | 21.3            | 20.2      | 19.5         | 79                         | 0.0                 |
| 16 March 2024 | 1017.8              | 22.4            | 20.7      | 19.5         | 88                         | Trace               |
| 17 March 2024 | 1016.4              | 26.8            | 23.1      | 20.7         | 86                         | 0.0                 |
| 18 March 2024 | 1016.2              | 23.0            | 21.0      | 19.8         | 92                         | 0.6                 |
| 19 March 2024 | 1019.5              | 24.6            | 21.2      | 19.5         | 69                         | 0.3                 |
| 20 March 2024 | 1022.4              | 24.3            | 20.8      | 18.3         | 54                         | 0.0                 |
| 21 March 2024 | 1017.9              | 23.8            | 20.7      | 18.4         | 65                         | Trace               |
| 22 March 2024 | 1013.3              | 25.9            | 22.5      | 20.4         | 83                         | Trace               |
| 23 March 2024 | 1012.8              | 29.1            | 24.7      | 22.1         | 84                         | 0.0                 |
| 24 March 2024 | 1014.7              | 31.5            | 26.4      | 24.5         | 77                         | 0.0                 |
| 25 March 2024 | 1014.5              | 28.9            | 25.9      | 23.8         | 79                         | 0.0                 |
| 26 March 2024 | 1017.0              | 30.3            | 26.2      | 23.7         | 79                         | 0.0                 |
| 27 March 2024 | 1018.5              | 25.1            | 22.4      | 20.8         | 82                         | Trace               |
| 28 March 2024 | 1013.9              | 27.9            | 24.7      | 22.4         | 82                         | 0.0                 |
| 29 March 2024 | 1013.8              | 30.0            | 25.5      | 23.0         | 81                         | Trace               |
| 30 March 2024 | 1013.5              | 30.8            | 26.4      | 24.3         | 80                         | Trace               |
| 31 March 2024 | 1011.1              | 27.8            | 27.1      | 26.0         | 84                         | 0.1                 |

Remark:

- Trace means rainfall less than 0.05 mm.

Source: Hong Kong Observatory

# Appendix J

---

Wind Data



**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 01 Mar 2024 00:00 | 3.3              | NWW            | 02 Mar 2024 00:00 | 3.0              | SE             |
| 01 Mar 2024 01:00 | 3.2              | SWW            | 02 Mar 2024 01:00 | 2.7              | SE             |
| 01 Mar 2024 02:00 | 2.8              | NWW            | 02 Mar 2024 02:00 | 3.9              | NEE            |
| 01 Mar 2024 03:00 | 2.7              | W              | 02 Mar 2024 03:00 | 3.1              | NE             |
| 01 Mar 2024 04:00 | 2.8              | S              | 02 Mar 2024 04:00 | 2.7              | NE             |
| 01 Mar 2024 05:00 | 3.0              | S              | 02 Mar 2024 05:00 | 2.8              | NE             |
| 01 Mar 2024 06:00 | 3.5              | N              | 02 Mar 2024 06:00 | 2.8              | NEE            |
| 01 Mar 2024 07:00 | 2.7              | NE             | 02 Mar 2024 07:00 | 3.0              | SEE            |
| 01 Mar 2024 08:00 | 2.9              | NE             | 02 Mar 2024 08:00 | 3.1              | NE             |
| 01 Mar 2024 09:00 | 3.3              | S              | 02 Mar 2024 09:00 | 3.0              | NEE            |
| 01 Mar 2024 10:00 | 2.9              | SW             | 02 Mar 2024 10:00 | 2.7              | S              |
| 01 Mar 2024 11:00 | 2.7              | E              | 02 Mar 2024 11:00 | 3.0              | SES            |
| 01 Mar 2024 12:00 | 2.9              | SWW            | 02 Mar 2024 12:00 | 4.0              | W              |
| 01 Mar 2024 13:00 | 3.2              | SEE            | 02 Mar 2024 13:00 | 3.0              | W              |
| 01 Mar 2024 14:00 | 3.1              | SWS            | 02 Mar 2024 14:00 | 3.1              | SWW            |
| 01 Mar 2024 15:00 | 2.8              | S              | 02 Mar 2024 15:00 | 3.2              | W              |
| 01 Mar 2024 16:00 | 3.3              | NE             | 02 Mar 2024 16:00 | 2.8              | W              |
| 01 Mar 2024 17:00 | 2.9              | SES            | 02 Mar 2024 17:00 | 2.7              | SW             |
| 01 Mar 2024 18:00 | 3.1              | SES            | 02 Mar 2024 18:00 | 2.7              | SW             |
| 01 Mar 2024 19:00 | 2.7              | S              | 02 Mar 2024 19:00 | 2.7              | NWW            |
| 01 Mar 2024 20:00 | 2.7              | NEN            | 02 Mar 2024 20:00 | 2.7              | S              |
| 01 Mar 2024 21:00 | 2.9              | NEN            | 02 Mar 2024 21:00 | 2.7              | NEN            |
| 01 Mar 2024 22:00 | 2.7              | NEN            | 02 Mar 2024 22:00 | 2.7              | NEE            |
| 01 Mar 2024 23:00 | 2.8              | SES            | 02 Mar 2024 23:00 | 2.7              | NEN            |

Wind Data (March 2024)

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 03 Mar 2024 00:00 | 2.7              | NE             | 04 Mar 2024 00:00 | 4.8              | NE             |
| 03 Mar 2024 01:00 | 2.7              | NEE            | 04 Mar 2024 01:00 | 5.2              | E              |
| 03 Mar 2024 02:00 | 2.7              | NEE            | 04 Mar 2024 02:00 | 5.3              | N              |
| 03 Mar 2024 03:00 | 2.7              | NE             | 04 Mar 2024 03:00 | 4.5              | NEE            |
| 03 Mar 2024 04:00 | 2.7              | NE             | 04 Mar 2024 04:00 | 6.2              | E              |
| 03 Mar 2024 05:00 | 2.8              | NE             | 04 Mar 2024 05:00 | 6.2              | N              |
| 03 Mar 2024 06:00 | 2.7              | NEE            | 04 Mar 2024 06:00 | 4.4              | NEN            |
| 03 Mar 2024 07:00 | 2.7              | NEE            | 04 Mar 2024 07:00 | 3.9              | SE             |
| 03 Mar 2024 08:00 | 3.2              | SEE            | 04 Mar 2024 08:00 | 2.9              | SE             |
| 03 Mar 2024 09:00 | 2.7              | NE             | 04 Mar 2024 09:00 | 4.4              | NEN            |
| 03 Mar 2024 10:00 | 2.7              | NE             | 04 Mar 2024 10:00 | 4.7              | N              |
| 03 Mar 2024 11:00 | 5.0              | E              | 04 Mar 2024 11:00 | 5.6              | NEN            |
| 03 Mar 2024 12:00 | 4.7              | NEE            | 04 Mar 2024 12:00 | 3.0              | NE             |
| 03 Mar 2024 13:00 | 3.4              | NEE            | 04 Mar 2024 13:00 | 3.5              | NEE            |
| 03 Mar 2024 14:00 | 3.0              | NEE            | 04 Mar 2024 14:00 | 3.7              | NE             |
| 03 Mar 2024 15:00 | 6.1              | NE             | 04 Mar 2024 15:00 | 3.3              | NEE            |
| 03 Mar 2024 16:00 | 5.7              | E              | 04 Mar 2024 16:00 | 2.9              | NEN            |
| 03 Mar 2024 17:00 | 6.3              | NEE            | 04 Mar 2024 17:00 | 2.9              | NEN            |
| 03 Mar 2024 18:00 | 4.7              | NE             | 04 Mar 2024 18:00 | 3.3              | NE             |
| 03 Mar 2024 19:00 | 5.6              | NEN            | 04 Mar 2024 19:00 | 2.9              | N              |
| 03 Mar 2024 20:00 | 5.6              | E              | 04 Mar 2024 20:00 | 3.4              | NEN            |
| 03 Mar 2024 21:00 | 5.0              | E              | 04 Mar 2024 21:00 | 3.5              | NE             |
| 03 Mar 2024 22:00 | 5.0              | NEE            | 04 Mar 2024 22:00 | 4.7              | SEE            |
| 03 Mar 2024 23:00 | 7.0              | SEE            | 04 Mar 2024 23:00 | 3.0              | NEN            |

Wind Data (March 2024)

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 05 Mar 2024 00:00 | 7.2              | NEN            | 06 Mar 2024 00:00 | 2.9              | SE             |
| 05 Mar 2024 01:00 | 3.1              | SES            | 06 Mar 2024 01:00 | 3.0              | W              |
| 05 Mar 2024 02:00 | 3.8              | NEN            | 06 Mar 2024 02:00 | 2.9              | SWS            |
| 05 Mar 2024 03:00 | 5.8              | NEN            | 06 Mar 2024 03:00 | 2.8              | E              |
| 05 Mar 2024 04:00 | 7.4              | NE             | 06 Mar 2024 04:00 | 2.8              | E              |
| 05 Mar 2024 05:00 | 9.0              | NEN            | 06 Mar 2024 05:00 | 2.8              | NEE            |
| 05 Mar 2024 06:00 | 7.5              | NE             | 06 Mar 2024 06:00 | 2.8              | E              |
| 05 Mar 2024 07:00 | 3.7              | NE             | 06 Mar 2024 07:00 | 2.8              | SEE            |
| 05 Mar 2024 08:00 | 3.0              | SEE            | 06 Mar 2024 08:00 | 2.8              | SWS            |
| 05 Mar 2024 09:00 | 3.3              | NEN            | 06 Mar 2024 09:00 | 2.7              | NEN            |
| 05 Mar 2024 10:00 | 6.5              | NE             | 06 Mar 2024 10:00 | 2.7              | NEN            |
| 05 Mar 2024 11:00 | 2.8              | E              | 06 Mar 2024 11:00 | 2.7              | NE             |
| 05 Mar 2024 12:00 | 5.9              | NEE            | 06 Mar 2024 12:00 | 2.9              | NE             |
| 05 Mar 2024 13:00 | 3.6              | SEE            | 06 Mar 2024 13:00 | 3.3              | SWS            |
| 05 Mar 2024 14:00 | 5.3              | SE             | 06 Mar 2024 14:00 | 3.0              | S              |
| 05 Mar 2024 15:00 | 7.6              | E              | 06 Mar 2024 15:00 | 2.8              | S              |
| 05 Mar 2024 16:00 | 4.9              | NEE            | 06 Mar 2024 16:00 | 2.8              | E              |
| 05 Mar 2024 17:00 | 5.6              | NE             | 06 Mar 2024 17:00 | 2.8              | SES            |
| 05 Mar 2024 18:00 | 5.4              | E              | 06 Mar 2024 18:00 | 2.7              | NEN            |
| 05 Mar 2024 19:00 | 4.2              | SE             | 06 Mar 2024 19:00 | 2.7              | NEN            |
| 05 Mar 2024 20:00 | 3.9              | N              | 06 Mar 2024 20:00 | 2.7              | NEE            |
| 05 Mar 2024 21:00 | 2.8              | NEE            | 06 Mar 2024 21:00 | 2.8              | NE             |
| 05 Mar 2024 22:00 | 2.9              | NEE            | 06 Mar 2024 22:00 | 2.9              | NEE            |
| 05 Mar 2024 23:00 | 2.9              | NEN            | 06 Mar 2024 23:00 | 2.7              | E              |

Wind Data (March 2024)

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 07 Mar 2024 00:00 | 2.7              | NEE            | 08 Mar 2024 00:00 | 2.9              | NEN            |
| 07 Mar 2024 01:00 | 2.8              | E              | 08 Mar 2024 01:00 | 2.7              | N              |
| 07 Mar 2024 02:00 | 2.9              | SEE            | 08 Mar 2024 02:00 | 3.7              | NEN            |
| 07 Mar 2024 03:00 | 2.8              | NEE            | 08 Mar 2024 03:00 | 2.8              | NE             |
| 07 Mar 2024 04:00 | 2.7              | NEE            | 08 Mar 2024 04:00 | 2.8              | SE             |
| 07 Mar 2024 05:00 | 3.1              | NEE            | 08 Mar 2024 05:00 | 2.7              | N              |
| 07 Mar 2024 06:00 | 2.7              | SEE            | 08 Mar 2024 06:00 | 2.7              | NEE            |
| 07 Mar 2024 07:00 | 2.6              | E              | 08 Mar 2024 07:00 | 3.0              | NE             |
| 07 Mar 2024 08:00 | 2.7              | N              | 08 Mar 2024 08:00 | 2.7              | NE             |
| 07 Mar 2024 09:00 | 2.7              | E              | 08 Mar 2024 09:00 | 2.9              | NEN            |
| 07 Mar 2024 10:00 | 2.7              | SEE            | 08 Mar 2024 10:00 | 2.7              | NE             |
| 07 Mar 2024 11:00 | 2.7              | E              | 08 Mar 2024 11:00 | 3.2              | E              |
| 07 Mar 2024 12:00 | 2.7              | NE             | 08 Mar 2024 12:00 | 3.6              | NEE            |
| 07 Mar 2024 13:00 | 2.7              | NEN            | 08 Mar 2024 13:00 | 2.7              | NE             |
| 07 Mar 2024 14:00 | 2.7              | SE             | 08 Mar 2024 14:00 | 3.8              | E              |
| 07 Mar 2024 15:00 | 2.7              | NE             | 08 Mar 2024 15:00 | 8.5              | NEE            |
| 07 Mar 2024 16:00 | 2.7              | NE             | 08 Mar 2024 16:00 | 3.9              | E              |
| 07 Mar 2024 17:00 | 2.7              | NEE            | 08 Mar 2024 17:00 | 2.9              | NEE            |
| 07 Mar 2024 18:00 | 2.8              | NE             | 08 Mar 2024 18:00 | 3.4              | N              |
| 07 Mar 2024 19:00 | 2.8              | N              | 08 Mar 2024 19:00 | 3.2              | E              |
| 07 Mar 2024 20:00 | 2.7              | E              | 08 Mar 2024 20:00 | 3.3              | NEE            |
| 07 Mar 2024 21:00 | 2.9              | NE             | 08 Mar 2024 21:00 | 3.1              | E              |
| 07 Mar 2024 22:00 | 2.9              | N              | 08 Mar 2024 22:00 | 3.0              | NEE            |
| 07 Mar 2024 23:00 | 3.0              | SES            | 08 Mar 2024 23:00 | 6.3              | E              |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 09 Mar 2024 00:00 | 7.2              | NEE            | 10 Mar 2024 00:00 | 3.1              | NEE            |
| 09 Mar 2024 01:00 | 10.0             | NE             | 10 Mar 2024 01:00 | 2.7              | NEN            |
| 09 Mar 2024 02:00 | 6.8              | NEE            | 10 Mar 2024 02:00 | 2.8              | SEE            |
| 09 Mar 2024 03:00 | 13.4             | NEN            | 10 Mar 2024 03:00 | 3.0              | NEN            |
| 09 Mar 2024 04:00 | 8.9              | NEN            | 10 Mar 2024 04:00 | 2.9              | NEE            |
| 09 Mar 2024 05:00 | 8.6              | NEE            | 10 Mar 2024 05:00 | 4.1              | NEE            |
| 09 Mar 2024 06:00 | 7.1              | NEE            | 10 Mar 2024 06:00 | 5.0              | NEN            |
| 09 Mar 2024 07:00 | 3.4              | N              | 10 Mar 2024 07:00 | 6.5              | E              |
| 09 Mar 2024 08:00 | 3.3              | E              | 10 Mar 2024 08:00 | 5.4              | N              |
| 09 Mar 2024 09:00 | 3.8              | SE             | 10 Mar 2024 09:00 | 5.8              | NEN            |
| 09 Mar 2024 10:00 | 3.8              | NEE            | 10 Mar 2024 10:00 | 3.9              | NEE            |
| 09 Mar 2024 11:00 | 4.4              | NEE            | 10 Mar 2024 11:00 | 5.3              | NEE            |
| 09 Mar 2024 12:00 | 4.6              | NE             | 10 Mar 2024 12:00 | 4.5              | NE             |
| 09 Mar 2024 13:00 | 3.6              | NEE            | 10 Mar 2024 13:00 | 3.3              | E              |
| 09 Mar 2024 14:00 | 4.0              | NE             | 10 Mar 2024 14:00 | 2.8              | NEN            |
| 09 Mar 2024 15:00 | 3.7              | NEN            | 10 Mar 2024 15:00 | 3.1              | SE             |
| 09 Mar 2024 16:00 | 3.4              | E              | 10 Mar 2024 16:00 | 5.2              | SW             |
| 09 Mar 2024 17:00 | 6.7              | NEE            | 10 Mar 2024 17:00 | 4.0              | N              |
| 09 Mar 2024 18:00 | 7.2              | NE             | 10 Mar 2024 18:00 | 3.7              | S              |
| 09 Mar 2024 19:00 | 3.9              | NEE            | 10 Mar 2024 19:00 | 3.6              | N              |
| 09 Mar 2024 20:00 | 3.9              | NEE            | 10 Mar 2024 20:00 | 3.2              | NE             |
| 09 Mar 2024 21:00 | 4.9              | NEE            | 10 Mar 2024 21:00 | 3.2              | NE             |
| 09 Mar 2024 22:00 | 6.5              | NE             | 10 Mar 2024 22:00 | 6.5              | NEN            |
| 09 Mar 2024 23:00 | 3.3              | NEN            | 10 Mar 2024 23:00 | 2.9              | NEN            |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 11 Mar 2024 00:00 | 5.3              | NE             | 12 Mar 2024 00:00 | 2.7              | N              |
| 11 Mar 2024 01:00 | 6.0              | NEN            | 12 Mar 2024 01:00 | 2.9              | SW             |
| 11 Mar 2024 02:00 | 8.0              | NE             | 12 Mar 2024 02:00 | 2.9              | SW             |
| 11 Mar 2024 03:00 | 4.4              | NE             | 12 Mar 2024 03:00 | 2.9              | SEE            |
| 11 Mar 2024 04:00 | 4.3              | NE             | 12 Mar 2024 04:00 | 3.1              | NE             |
| 11 Mar 2024 05:00 | 3.6              | NE             | 12 Mar 2024 05:00 | 2.7              | SEE            |
| 11 Mar 2024 06:00 | 3.5              | SE             | 12 Mar 2024 06:00 | 2.6              | NE             |
| 11 Mar 2024 07:00 | 4.6              | NEE            | 12 Mar 2024 07:00 | 2.7              | E              |
| 11 Mar 2024 08:00 | 5.2              | NEE            | 12 Mar 2024 08:00 | 2.7              | NEE            |
| 11 Mar 2024 09:00 | 3.4              | SEE            | 12 Mar 2024 09:00 | 2.7              | NEN            |
| 11 Mar 2024 10:00 | 3.8              | S              | 12 Mar 2024 10:00 | 2.7              | NEE            |
| 11 Mar 2024 11:00 | 3.9              | E              | 12 Mar 2024 11:00 | 3.3              | N              |
| 11 Mar 2024 12:00 | 3.7              | S              | 12 Mar 2024 12:00 | 5.7              | NEE            |
| 11 Mar 2024 13:00 | 3.6              | SEE            | 12 Mar 2024 13:00 | 8.8              | NEE            |
| 11 Mar 2024 14:00 | 2.8              | SWS            | 12 Mar 2024 14:00 | 5.6              | E              |
| 11 Mar 2024 15:00 | 2.7              | W              | 12 Mar 2024 15:00 | 3.5              | E              |
| 11 Mar 2024 16:00 | 3.9              | SW             | 12 Mar 2024 16:00 | 4.4              | E              |
| 11 Mar 2024 17:00 | 2.7              | SWW            | 12 Mar 2024 17:00 | 3.4              | NEE            |
| 11 Mar 2024 18:00 | 2.7              | W              | 12 Mar 2024 18:00 | 3.2              | NEN            |
| 11 Mar 2024 19:00 | 2.8              | W              | 12 Mar 2024 19:00 | 3.4              | NEE            |
| 11 Mar 2024 20:00 | 2.8              | SWS            | 12 Mar 2024 20:00 | 2.7              | E              |
| 11 Mar 2024 21:00 | 2.8              | S              | 12 Mar 2024 21:00 | 2.7              | E              |
| 11 Mar 2024 22:00 | 2.8              | SW             | 12 Mar 2024 22:00 | 2.7              | E              |
| 11 Mar 2024 23:00 | 2.7              | SEE            | 12 Mar 2024 23:00 | 4.4              | NEE            |

Wind Data (March 2024)

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 13 Mar 2024 00:00 | 3.8              | NEE            | 14 Mar 2024 00:00 | 3.1              | NEE            |
| 13 Mar 2024 01:00 | 4.3              | NEN            | 14 Mar 2024 01:00 | 2.7              | NE             |
| 13 Mar 2024 02:00 | 3.7              | NE             | 14 Mar 2024 02:00 | 4.4              | E              |
| 13 Mar 2024 03:00 | 2.7              | NEE            | 14 Mar 2024 03:00 | 2.8              | NEE            |
| 13 Mar 2024 04:00 | 2.7              | NEE            | 14 Mar 2024 04:00 | 4.1              | E              |
| 13 Mar 2024 05:00 | 2.7              | NEE            | 14 Mar 2024 05:00 | 2.9              | NE             |
| 13 Mar 2024 06:00 | 3.0              | E              | 14 Mar 2024 06:00 | 5.5              | NEE            |
| 13 Mar 2024 07:00 | 2.7              | NEE            | 14 Mar 2024 07:00 | 3.6              | E              |
| 13 Mar 2024 08:00 | 2.7              | NEE            | 14 Mar 2024 08:00 | 4.8              | NE             |
| 13 Mar 2024 09:00 | 4.0              | NEE            | 14 Mar 2024 09:00 | 4.7              | E              |
| 13 Mar 2024 10:00 | 6.1              | SE             | 14 Mar 2024 10:00 | 3.6              | E              |
| 13 Mar 2024 11:00 | 7.5              | NE             | 14 Mar 2024 11:00 | 3.9              | NEE            |
| 13 Mar 2024 12:00 | 12.1             | NEE            | 14 Mar 2024 12:00 | 4.8              | NEN            |
| 13 Mar 2024 13:00 | 8.8              | NEE            | 14 Mar 2024 13:00 | 4.4              | NEE            |
| 13 Mar 2024 14:00 | 3.9              | NEE            | 14 Mar 2024 14:00 | 4.0              | E              |
| 13 Mar 2024 15:00 | 4.4              | E              | 14 Mar 2024 15:00 | 2.7              | NEE            |
| 13 Mar 2024 16:00 | 2.7              | NE             | 14 Mar 2024 16:00 | 5.0              | NE             |
| 13 Mar 2024 17:00 | 6.5              | NEE            | 14 Mar 2024 17:00 | 2.7              | NEE            |
| 13 Mar 2024 18:00 | 4.1              | NEE            | 14 Mar 2024 18:00 | 2.7              | NEE            |
| 13 Mar 2024 19:00 | 2.9              | NEN            | 14 Mar 2024 19:00 | 2.8              | NEE            |
| 13 Mar 2024 20:00 | 2.8              | NE             | 14 Mar 2024 20:00 | 3.5              | NEE            |
| 13 Mar 2024 21:00 | 2.8              | NEE            | 14 Mar 2024 21:00 | 2.8              | E              |
| 13 Mar 2024 22:00 | 3.0              | NEE            | 14 Mar 2024 22:00 | 2.8              | NEE            |
| 13 Mar 2024 23:00 | 2.7              | NEN            | 14 Mar 2024 23:00 | 2.7              | E              |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 15 Mar 2024 00:00 | 2.7              | NEN            | 16 Mar 2024 00:00 | 3.8              | E              |
| 15 Mar 2024 01:00 | 2.7              | NEE            | 16 Mar 2024 01:00 | 4.0              | NE             |
| 15 Mar 2024 02:00 | 2.8              | SE             | 16 Mar 2024 02:00 | 3.6              | NE             |
| 15 Mar 2024 03:00 | 2.7              | NEE            | 16 Mar 2024 03:00 | 2.8              | E              |
| 15 Mar 2024 04:00 | 2.8              | N              | 16 Mar 2024 04:00 | 2.8              | NE             |
| 15 Mar 2024 05:00 | 2.7              | SEE            | 16 Mar 2024 05:00 | 3.0              | SEE            |
| 15 Mar 2024 06:00 | 2.8              | NEE            | 16 Mar 2024 06:00 | 2.8              | E              |
| 15 Mar 2024 07:00 | 3.8              | NE             | 16 Mar 2024 07:00 | 4.3              | NEE            |
| 15 Mar 2024 08:00 | 3.3              | NE             | 16 Mar 2024 08:00 | 2.7              | NEN            |
| 15 Mar 2024 09:00 | 3.3              | E              | 16 Mar 2024 09:00 | 2.7              | SE             |
| 15 Mar 2024 10:00 | 2.8              | E              | 16 Mar 2024 10:00 | 2.7              | E              |
| 15 Mar 2024 11:00 | 5.2              | NEE            | 16 Mar 2024 11:00 | 2.8              | E              |
| 15 Mar 2024 12:00 | 3.6              | NEE            | 16 Mar 2024 12:00 | 2.7              | SES            |
| 15 Mar 2024 13:00 | 2.8              | E              | 16 Mar 2024 13:00 | 2.7              | NEN            |
| 15 Mar 2024 14:00 | 4.3              | E              | 16 Mar 2024 14:00 | 2.7              | SEE            |
| 15 Mar 2024 15:00 | 3.0              | NEE            | 16 Mar 2024 15:00 | 2.7              | SE             |
| 15 Mar 2024 16:00 | 3.6              | NEE            | 16 Mar 2024 16:00 | 2.7              | NEN            |
| 15 Mar 2024 17:00 | 2.8              | E              | 16 Mar 2024 17:00 | 2.8              | NEN            |
| 15 Mar 2024 18:00 | 3.6              | NE             | 16 Mar 2024 18:00 | 3.5              | NEE            |
| 15 Mar 2024 19:00 | 3.0              | N              | 16 Mar 2024 19:00 | 4.2              | E              |
| 15 Mar 2024 20:00 | 2.7              | NE             | 16 Mar 2024 20:00 | 2.8              | NEE            |
| 15 Mar 2024 21:00 | 4.9              | NE             | 16 Mar 2024 21:00 | 2.7              | SE             |
| 15 Mar 2024 22:00 | 6.2              | NEE            | 16 Mar 2024 22:00 | 2.7              | NEE            |
| 15 Mar 2024 23:00 | 3.1              | E              | 16 Mar 2024 23:00 | 2.7              | SWS            |



**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 17 Mar 2024 00:00 | 2.7              | E              | 18 Mar 2024 00:00 | 2.7              | SEE            |
| 17 Mar 2024 01:00 | 2.7              | SES            | 18 Mar 2024 01:00 | 2.7              | NE             |
| 17 Mar 2024 02:00 | 2.7              | NEE            | 18 Mar 2024 02:00 | 2.7              | SES            |
| 17 Mar 2024 03:00 | 2.7              | SWW            | 18 Mar 2024 03:00 | 2.8              | SE             |
| 17 Mar 2024 04:00 | 2.7              | NEE            | 18 Mar 2024 04:00 | 2.7              | N              |
| 17 Mar 2024 05:00 | 2.7              | SW             | 18 Mar 2024 05:00 | 2.8              | SEE            |
| 17 Mar 2024 06:00 | 2.7              | SWS            | 18 Mar 2024 06:00 | 2.8              | NEE            |
| 17 Mar 2024 07:00 | 2.7              | N              | 18 Mar 2024 07:00 | 2.7              | SEE            |
| 17 Mar 2024 08:00 | 2.7              | SES            | 18 Mar 2024 08:00 | 2.7              | NEN            |
| 17 Mar 2024 09:00 | 2.7              | SES            | 18 Mar 2024 09:00 | 2.7              | NE             |
| 17 Mar 2024 10:00 | 2.7              | NE             | 18 Mar 2024 10:00 | 3.2              | E              |
| 17 Mar 2024 11:00 | 2.7              | E              | 18 Mar 2024 11:00 | 2.7              | SE             |
| 17 Mar 2024 12:00 | 8.8              | NEE            | 18 Mar 2024 12:00 | 2.7              | SES            |
| 17 Mar 2024 13:00 | 3.3              | SEE            | 18 Mar 2024 13:00 | 4.0              | NE             |
| 17 Mar 2024 14:00 | 8.1              | NEN            | 18 Mar 2024 14:00 | 3.7              | N              |
| 17 Mar 2024 15:00 | 6.8              | SEE            | 18 Mar 2024 15:00 | 2.7              | SEE            |
| 17 Mar 2024 16:00 | 4.2              | NE             | 18 Mar 2024 16:00 | 4.2              | NEN            |
| 17 Mar 2024 17:00 | 2.8              | SE             | 18 Mar 2024 17:00 | 3.1              | N              |
| 17 Mar 2024 18:00 | 3.2              | NEN            | 18 Mar 2024 18:00 | 2.7              | SEE            |
| 17 Mar 2024 19:00 | 2.7              | NEN            | 18 Mar 2024 19:00 | 3.4              | E              |
| 17 Mar 2024 20:00 | 2.7              | NE             | 18 Mar 2024 20:00 | 2.9              | NEN            |
| 17 Mar 2024 21:00 | 2.7              | NEE            | 18 Mar 2024 21:00 | 2.7              | NEN            |
| 17 Mar 2024 22:00 | 2.7              | NE             | 18 Mar 2024 22:00 | 2.8              | NEE            |
| 17 Mar 2024 23:00 | 2.7              | E              | 18 Mar 2024 23:00 | 3.9              | NEE            |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 19 Mar 2024 00:00 | 2.6              | NE             | 20 Mar 2024 00:00 | 2.7              | NEE            |
| 19 Mar 2024 01:00 | 2.7              | NE             | 20 Mar 2024 01:00 | 2.7              | NEN            |
| 19 Mar 2024 02:00 | 2.7              | NEE            | 20 Mar 2024 02:00 | 2.8              | NE             |
| 19 Mar 2024 03:00 | 2.7              | S              | 20 Mar 2024 03:00 | 3.0              | NEN            |
| 19 Mar 2024 04:00 | 2.7              | SEE            | 20 Mar 2024 04:00 | 2.7              | NE             |
| 19 Mar 2024 05:00 | 2.8              | E              | 20 Mar 2024 05:00 | 2.7              | SEE            |
| 19 Mar 2024 06:00 | 3.2              | N              | 20 Mar 2024 06:00 | 2.7              | NEE            |
| 19 Mar 2024 07:00 | 3.0              | E              | 20 Mar 2024 07:00 | 2.7              | N              |
| 19 Mar 2024 08:00 | 4.1              | NEE            | 20 Mar 2024 08:00 | 2.7              | N              |
| 19 Mar 2024 09:00 | 3.5              | E              | 20 Mar 2024 09:00 | 2.7              | NEN            |
| 19 Mar 2024 10:00 | 2.8              | N              | 20 Mar 2024 10:00 | 2.6              | NEN            |
| 19 Mar 2024 11:00 | 2.7              | NEE            | 20 Mar 2024 11:00 | 2.7              | E              |
| 19 Mar 2024 12:00 | 2.8              | E              | 20 Mar 2024 12:00 | 5.4              | NE             |
| 19 Mar 2024 13:00 | 2.8              | NEN            | 20 Mar 2024 13:00 | 3.9              | SEE            |
| 19 Mar 2024 14:00 | 2.7              | N              | 20 Mar 2024 14:00 | 9.6              | E              |
| 19 Mar 2024 15:00 | 2.8              | NEE            | 20 Mar 2024 15:00 | 3.8              | NEE            |
| 19 Mar 2024 16:00 | 2.7              | NE             | 20 Mar 2024 16:00 | 7.2              | E              |
| 19 Mar 2024 17:00 | 2.7              | NEN            | 20 Mar 2024 17:00 | 2.8              | SEE            |
| 19 Mar 2024 18:00 | 2.7              | W              | 20 Mar 2024 18:00 | 3.1              | E              |
| 19 Mar 2024 19:00 | 2.7              | NW             | 20 Mar 2024 19:00 | 2.7              | NE             |
| 19 Mar 2024 20:00 | 2.7              | NW             | 20 Mar 2024 20:00 | 2.7              | NE             |
| 19 Mar 2024 21:00 | 2.7              | NW             | 20 Mar 2024 21:00 | 3.0              | NEE            |
| 19 Mar 2024 22:00 | 2.7              | SWW            | 20 Mar 2024 22:00 | 2.8              | NE             |
| 19 Mar 2024 23:00 | 2.9              | SE             | 20 Mar 2024 23:00 | 2.8              | E              |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 21 Mar 2024 00:00 | 3.0              | NE             | 22 Mar 2024 00:00 | 2.8              | E              |
| 21 Mar 2024 01:00 | 4.5              | NEN            | 22 Mar 2024 01:00 | 3.4              | NE             |
| 21 Mar 2024 02:00 | 4.6              | E              | 22 Mar 2024 02:00 | 3.9              | NEN            |
| 21 Mar 2024 03:00 | 2.8              | E              | 22 Mar 2024 03:00 | 4.8              | S              |
| 21 Mar 2024 04:00 | 3.2              | E              | 22 Mar 2024 04:00 | 7.2              | SEE            |
| 21 Mar 2024 05:00 | 3.0              | E              | 22 Mar 2024 05:00 | 5.0              | E              |
| 21 Mar 2024 06:00 | 2.9              | E              | 22 Mar 2024 06:00 | 3.8              | E              |
| 21 Mar 2024 07:00 | 2.8              | E              | 22 Mar 2024 07:00 | 3.1              | NEE            |
| 21 Mar 2024 08:00 | 3.6              | NEE            | 22 Mar 2024 08:00 | 3.0              | NE             |
| 21 Mar 2024 09:00 | 3.8              | NE             | 22 Mar 2024 09:00 | 2.9              | E              |
| 21 Mar 2024 10:00 | 4.6              | NEE            | 22 Mar 2024 10:00 | 2.7              | SEE            |
| 21 Mar 2024 11:00 | 2.9              | NEN            | 22 Mar 2024 11:00 | 3.3              | NE             |
| 21 Mar 2024 12:00 | 3.9              | NE             | 22 Mar 2024 12:00 | 6.8              | E              |
| 21 Mar 2024 13:00 | 6.1              | NE             | 22 Mar 2024 13:00 | 3.5              | NEN            |
| 21 Mar 2024 14:00 | 4.8              | NEE            | 22 Mar 2024 14:00 | 3.8              | N              |
| 21 Mar 2024 15:00 | 7.0              | E              | 22 Mar 2024 15:00 | 7.4              | NEE            |
| 21 Mar 2024 16:00 | 3.2              | NEE            | 22 Mar 2024 16:00 | 6.0              | E              |
| 21 Mar 2024 17:00 | 2.9              | NEE            | 22 Mar 2024 17:00 | 6.4              | E              |
| 21 Mar 2024 18:00 | 3.6              | SEE            | 22 Mar 2024 18:00 | 7.0              | NE             |
| 21 Mar 2024 19:00 | 2.7              | NEE            | 22 Mar 2024 19:00 | 3.6              | E              |
| 21 Mar 2024 20:00 | 3.2              | SEE            | 22 Mar 2024 20:00 | 4.3              | NE             |
| 21 Mar 2024 21:00 | 3.0              | E              | 22 Mar 2024 21:00 | 2.8              | N              |
| 21 Mar 2024 22:00 | 2.7              | NE             | 22 Mar 2024 22:00 | 3.3              | SEE            |
| 21 Mar 2024 23:00 | 2.7              | NEN            | 22 Mar 2024 23:00 | 2.9              | NEE            |

Wind Data (March 2024)

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 23 Mar 2024 00:00 | 3.1              | E              | 24 Mar 2024 00:00 | 3.9              | SEE            |
| 23 Mar 2024 01:00 | 2.8              | NEN            | 24 Mar 2024 01:00 | 2.8              | SEE            |
| 23 Mar 2024 02:00 | 2.9              | NE             | 24 Mar 2024 02:00 | 6.1              | N              |
| 23 Mar 2024 03:00 | 2.9              | E              | 24 Mar 2024 03:00 | 3.3              | NEE            |
| 23 Mar 2024 04:00 | 2.9              | SEE            | 24 Mar 2024 04:00 | 3.8              | E              |
| 23 Mar 2024 05:00 | 2.9              | SES            | 24 Mar 2024 05:00 | 2.9              | N              |
| 23 Mar 2024 06:00 | 2.8              | NEE            | 24 Mar 2024 06:00 | 3.3              | NEN            |
| 23 Mar 2024 07:00 | 2.8              | NEE            | 24 Mar 2024 07:00 | 3.0              | NE             |
| 23 Mar 2024 08:00 | 2.8              | SE             | 24 Mar 2024 08:00 | 3.2              | N              |
| 23 Mar 2024 09:00 | 2.7              | NE             | 24 Mar 2024 09:00 | 5.0              | NEN            |
| 23 Mar 2024 10:00 | 2.7              | SEE            | 24 Mar 2024 10:00 | 7.6              | NEE            |
| 23 Mar 2024 11:00 | 2.7              | NEE            | 24 Mar 2024 11:00 | 6.7              | SE             |
| 23 Mar 2024 12:00 | 4.5              | NEE            | 24 Mar 2024 12:00 | 15.8             | NEE            |
| 23 Mar 2024 13:00 | 5.1              | NEE            | 24 Mar 2024 13:00 | 4.2              | E              |
| 23 Mar 2024 14:00 | 4.6              | E              | 24 Mar 2024 14:00 | 6.1              | E              |
| 23 Mar 2024 15:00 | 5.2              | E              | 24 Mar 2024 15:00 | 9.1              | SEE            |
| 23 Mar 2024 16:00 | 5.0              | NEE            | 24 Mar 2024 16:00 | 6.0              | SEE            |
| 23 Mar 2024 17:00 | 3.5              | E              | 24 Mar 2024 17:00 | 4.6              | NEE            |
| 23 Mar 2024 18:00 | 3.2              | E              | 24 Mar 2024 18:00 | 3.9              | NE             |
| 23 Mar 2024 19:00 | 3.0              | NEN            | 24 Mar 2024 19:00 | 4.4              | E              |
| 23 Mar 2024 20:00 | 2.9              | SE             | 24 Mar 2024 20:00 | 2.9              | NEE            |
| 23 Mar 2024 21:00 | 4.9              | NEE            | 24 Mar 2024 21:00 | 2.7              | NEE            |
| 23 Mar 2024 22:00 | 2.9              | S              | 24 Mar 2024 22:00 | 2.8              | SES            |
| 23 Mar 2024 23:00 | 3.2              | NEN            | 24 Mar 2024 23:00 | 2.9              | E              |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 25 Mar 2024 00:00 | 2.7              | NEN            | 26 Mar 2024 00:00 | 2.8              | NE             |
| 25 Mar 2024 01:00 | 2.7              | NEE            | 26 Mar 2024 01:00 | 2.7              | NEN            |
| 25 Mar 2024 02:00 | 2.7              | SES            | 26 Mar 2024 02:00 | 2.7              | NEE            |
| 25 Mar 2024 03:00 | 2.7              | S              | 26 Mar 2024 03:00 | 2.7              | SEE            |
| 25 Mar 2024 04:00 | 2.7              | SEE            | 26 Mar 2024 04:00 | 2.7              | SEE            |
| 25 Mar 2024 05:00 | 2.7              | SES            | 26 Mar 2024 05:00 | 2.7              | E              |
| 25 Mar 2024 06:00 | 2.7              | SES            | 26 Mar 2024 06:00 | 2.7              | SES            |
| 25 Mar 2024 07:00 | 2.7              | NEN            | 26 Mar 2024 07:00 | 2.7              | SES            |
| 25 Mar 2024 08:00 | 3.5              | SEE            | 26 Mar 2024 08:00 | 2.7              | NEN            |
| 25 Mar 2024 09:00 | 3.0              | NE             | 26 Mar 2024 09:00 | 2.7              | NE             |
| 25 Mar 2024 10:00 | 2.7              | SEE            | 26 Mar 2024 10:00 | 2.7              | NEN            |
| 25 Mar 2024 11:00 | 2.7              | E              | 26 Mar 2024 11:00 | 2.7              | SEE            |
| 25 Mar 2024 12:00 | 3.0              | E              | 26 Mar 2024 12:00 | 2.7              | NE             |
| 25 Mar 2024 13:00 | 2.7              | SE             | 26 Mar 2024 13:00 | 3.6              | E              |
| 25 Mar 2024 14:00 | 2.7              | NE             | 26 Mar 2024 14:00 | 3.8              | NEE            |
| 25 Mar 2024 15:00 | 3.2              | SES            | 26 Mar 2024 15:00 | 4.8              | NE             |
| 25 Mar 2024 16:00 | 2.7              | E              | 26 Mar 2024 16:00 | 5.0              | E              |
| 25 Mar 2024 17:00 | 2.7              | SE             | 26 Mar 2024 17:00 | 3.9              | SEE            |
| 25 Mar 2024 18:00 | 2.7              | NEE            | 26 Mar 2024 18:00 | 4.7              | E              |
| 25 Mar 2024 19:00 | 2.7              | N              | 26 Mar 2024 19:00 | 3.9              | E              |
| 25 Mar 2024 20:00 | 2.7              | NE             | 26 Mar 2024 20:00 | 4.8              | SEE            |
| 25 Mar 2024 21:00 | 2.7              | NEE            | 26 Mar 2024 21:00 | 3.8              | E              |
| 25 Mar 2024 22:00 | 2.8              | N              | 26 Mar 2024 22:00 | 3.4              | NEE            |
| 25 Mar 2024 23:00 | 2.8              | SEE            | 26 Mar 2024 23:00 | 4.9              | E              |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 27 Mar 2024 00:00 | 3.0              | NEN            | 28 Mar 2024 00:00 | 2.7              | NEN            |
| 27 Mar 2024 01:00 | 6.5              | SEE            | 28 Mar 2024 01:00 | 3.3              | NE             |
| 27 Mar 2024 02:00 | 5.8              | NEE            | 28 Mar 2024 02:00 | 2.7              | NEE            |
| 27 Mar 2024 03:00 | 3.0              | SEE            | 28 Mar 2024 03:00 | 2.7              | N              |
| 27 Mar 2024 04:00 | 2.8              | NEE            | 28 Mar 2024 04:00 | 2.7              | NE             |
| 27 Mar 2024 05:00 | 2.7              | NE             | 28 Mar 2024 05:00 | 2.7              | NEE            |
| 27 Mar 2024 06:00 | 2.7              | NEE            | 28 Mar 2024 06:00 | 2.7              | NEN            |
| 27 Mar 2024 07:00 | 3.1              | NE             | 28 Mar 2024 07:00 | 2.7              | SES            |
| 27 Mar 2024 08:00 | 3.7              | SE             | 28 Mar 2024 08:00 | 2.7              | NEN            |
| 27 Mar 2024 09:00 | 2.7              | SWW            | 28 Mar 2024 09:00 | 2.7              | NEN            |
| 27 Mar 2024 10:00 | 5.8              | NEE            | 28 Mar 2024 10:00 | 2.7              | N              |
| 27 Mar 2024 11:00 | 3.1              | SES            | 28 Mar 2024 11:00 | 2.7              | SEE            |
| 27 Mar 2024 12:00 | 3.1              | SE             | 28 Mar 2024 12:00 | 2.6              | SEE            |
| 27 Mar 2024 13:00 | 7.1              | N              | 28 Mar 2024 13:00 | 2.7              | SEE            |
| 27 Mar 2024 14:00 | 4.8              | E              | 28 Mar 2024 14:00 | 2.7              | SEE            |
| 27 Mar 2024 15:00 | 3.7              | NEE            | 28 Mar 2024 15:00 | 2.7              | SEE            |
| 27 Mar 2024 16:00 | 3.8              | NEE            | 28 Mar 2024 16:00 | 2.7              | E              |
| 27 Mar 2024 17:00 | 4.2              | SEE            | 28 Mar 2024 17:00 | 2.7              | E              |
| 27 Mar 2024 18:00 | 3.1              | SE             | 28 Mar 2024 18:00 | 2.7              | S              |
| 27 Mar 2024 19:00 | 3.9              | NEN            | 28 Mar 2024 19:00 | 2.7              | SWS            |
| 27 Mar 2024 20:00 | 4.8              | SE             | 28 Mar 2024 20:00 | 2.7              | E              |
| 27 Mar 2024 21:00 | 4.7              | SWS            | 28 Mar 2024 21:00 | 2.6              | NEE            |
| 27 Mar 2024 22:00 | 3.0              | NEN            | 28 Mar 2024 22:00 | 2.7              | NEE            |
| 27 Mar 2024 23:00 | 4.6              | SEE            | 28 Mar 2024 23:00 | 2.7              | NEE            |

**Wind Data (March 2024)**

| Date & Time       | Wind Speed (m/s) | Wind Direction | Date & Time       | Wind Speed (m/s) | Wind Direction |
|-------------------|------------------|----------------|-------------------|------------------|----------------|
| 29 Mar 2024 00:00 | 2.7              | SEE            | 30 Mar 2024 00:00 | 2.7              | E              |
| 29 Mar 2024 01:00 | 2.7              | SEE            | 30 Mar 2024 01:00 | 2.7              | E              |
| 29 Mar 2024 02:00 | 2.6              | SE             | 30 Mar 2024 02:00 | 2.7              | NEE            |
| 29 Mar 2024 03:00 | 2.6              | NEN            | 30 Mar 2024 03:00 | 2.7              | SEE            |
| 29 Mar 2024 04:00 | 2.7              | SE             | 30 Mar 2024 04:00 | 2.7              | NEN            |
| 29 Mar 2024 05:00 | 2.6              | E              | 30 Mar 2024 05:00 | 2.7              | E              |
| 29 Mar 2024 06:00 | 2.7              | NE             | 30 Mar 2024 06:00 | 2.7              | E              |
| 29 Mar 2024 07:00 | 2.7              | NE             | 30 Mar 2024 07:00 | 2.7              | SEE            |
| 29 Mar 2024 08:00 | 2.7              | E              | 30 Mar 2024 08:00 | 3.3              | E              |
| 29 Mar 2024 09:00 | 2.6              | SE             | 30 Mar 2024 09:00 | 3.4              | SWS            |
| 29 Mar 2024 10:00 | 2.7              | NEE            | 30 Mar 2024 10:00 | 3.8              | SE             |
| 29 Mar 2024 11:00 | 2.7              | NEE            | 30 Mar 2024 11:00 | 4.2              | E              |
| 29 Mar 2024 12:00 | 2.7              | SEE            | 30 Mar 2024 12:00 | 3.3              | NE             |
| 29 Mar 2024 13:00 | 2.8              | NE             | 30 Mar 2024 13:00 | 4.6              | E              |
| 29 Mar 2024 14:00 | 6.6              | E              | 30 Mar 2024 14:00 | 6.3              | SEE            |
| 29 Mar 2024 15:00 | 3.3              | NEE            | 30 Mar 2024 15:00 | 6.9              | SE             |
| 29 Mar 2024 16:00 | 12.5             | SEE            | 30 Mar 2024 16:00 | 5.6              | NE             |
| 29 Mar 2024 17:00 | 4.6              | NEE            | 30 Mar 2024 17:00 | 3.0              | SEE            |
| 29 Mar 2024 18:00 | 8.5              | SEE            | 30 Mar 2024 18:00 | 3.4              | SES            |
| 29 Mar 2024 19:00 | 3.0              | E              | 30 Mar 2024 19:00 | 2.8              | S              |
| 29 Mar 2024 20:00 | 2.7              | E              | 30 Mar 2024 20:00 | 2.9              | SE             |
| 29 Mar 2024 21:00 | 2.7              | SEE            | 30 Mar 2024 21:00 | 2.8              | SES            |
| 29 Mar 2024 22:00 | 2.7              | NEE            | 30 Mar 2024 22:00 | 3.2              | SWS            |
| 29 Mar 2024 23:00 | 2.7              | NEN            | 30 Mar 2024 23:00 | 4.7              | E              |

Wind Data (March 2024)

| Date & Time       | Wind Speed<br>(m/s) | Wind<br>Direction | Date & Time | Wind Speed<br>(m/s) | Wind<br>Direction |
|-------------------|---------------------|-------------------|-------------|---------------------|-------------------|
| 31 Mar 2024 00:00 | 2.7                 | NEE               |             |                     |                   |
| 31 Mar 2024 01:00 | 2.6                 | NEE               |             |                     |                   |
| 31 Mar 2024 02:00 | 2.7                 | E                 |             |                     |                   |
| 31 Mar 2024 03:00 | 4.8                 | NE                |             |                     |                   |
| 31 Mar 2024 04:00 | 2.7                 | S                 |             |                     |                   |
| 31 Mar 2024 05:00 | 2.7                 | NE                |             |                     |                   |
| 31 Mar 2024 06:00 | 2.7                 | NEE               |             |                     |                   |
| 31 Mar 2024 07:00 | 3.7                 | NE                |             |                     |                   |
| 31 Mar 2024 08:00 | 10.0                | SE                |             |                     |                   |
| 31 Mar 2024 09:00 | 6.2                 | NEN               |             |                     |                   |
| 31 Mar 2024 10:00 | 5.4                 | N                 |             |                     |                   |
| 31 Mar 2024 11:00 | 3.4                 | NEN               |             |                     |                   |
| 31 Mar 2024 12:00 | 5.9                 | SWS               |             |                     |                   |
| 31 Mar 2024 13:00 | 3.0                 | NE                |             |                     |                   |
| 31 Mar 2024 14:00 | 3.6                 | E                 |             |                     |                   |
| 31 Mar 2024 15:00 | 6.0                 | NE                |             |                     |                   |
| 31 Mar 2024 16:00 | 7.7                 | SE                |             |                     |                   |
| 31 Mar 2024 17:00 | 2.7                 | SES               |             |                     |                   |
| 31 Mar 2024 18:00 | 3.4                 | NEE               |             |                     |                   |
| 31 Mar 2024 19:00 | 4.1                 | N                 |             |                     |                   |
| 31 Mar 2024 20:00 | 3.1                 | E                 |             |                     |                   |
| 31 Mar 2024 21:00 | 3.0                 | N                 |             |                     |                   |
| 31 Mar 2024 22:00 | 2.7                 | NEE               |             |                     |                   |
| 31 Mar 2024 23:00 | 2.7                 | NEE               |             |                     |                   |



# Appendix K

---

Summary of ET's Site Environmental  
Audit in the Reporting Month



### Summary of ET's Site Environmental Audit in the Reporting Month

| Parameters                    | Date          | Observations and Recommendations                                    | Follow-up     |
|-------------------------------|---------------|---|---------------|
| Air Quality                   | NA            |   |               |
| Noise                         | NA            |   |               |
| Water Quality                 | NA            |   |               |
| Chemical and Waste Management | 21 March 2024 | Drip tray should be provided for the chemical container.            | 21 March 2024 |
| Landscape and Visual Impact   | NA            |   |               |
| Permit / Licenses             | 25 March 2024 | The excavator in the landscape works should provide the NRMM label. | 25 March 2024 |
| Others                        | NA            |   |               |

Date of Inspection: 21 March 2024

| Defect Photo  | Rectified Photo  |
|---|--|
|  |  |
| Reminder 1:<br>Drip tray should be provided for the chemical container.           | Chemical container was removed in the area.  |

Date of Inspection: 25 March 2024

| Defect Photo  | Rectified Photo  |
|---|--|
|  |  |
| Reminder 1:<br>The excavator in the landscape works should provide the NRMM label.  | NRMM label was provided.   |

# Appendix L

---

## Waste Flow Table

Waste Flow Table (2024)

| Monthly<br>Ending | Actual Quantities of Inert C&D Materials Generated Monthly |  |                           |                             |                            |               | Actual Quantities of C&D<br>Wastes Generated |                   | Actual Quantities of Recyclables Generation |             |                                   |             |
|-------------------|--|--|---------------------------|-----------------------------|----------------------------|---------------|--|-------------------|---|-------------|-----------------------------------|-------------|
|                   | Total<br>Quantity<br>Generated                             | Hard Rock<br>and Large<br>Broken<br>Concrete | Reused in the<br>Contract | Reused in<br>other Projects | Disposed as<br>Public Fill | Imported Fill | Chemical<br>Waste                            | General<br>Refuse | Felled Trees                                | Metals      | Paper /<br>Cardboard<br>Packaging | Plastics    |
|                   | (in '000m3)  | (in '000m3)                                  | (in '000m3)               | (in '000m3)                 | (in '000m3)                | (in '000m3)   | (in '000kg)                                  | (in '000kg)       | (in '000kg)                                 | (in '000kg) | (in '000kg)                       | (in '000kg) |
| 2024 Jan          | 0.186  | 0.000  | 0.000                     | 0.000                       | 0.186                      | 0.000         | 0.000  | 14.060            | 0.000                                       | 0.000       | 0.000                             | 0.000       |
| 2024 Feb          | 0.015  | 0.000  | 0.000                     | 0.000                       | 0.015                      | 0.000         | 0.000  | 5.040             | 0.000                                       | 0.000       | 0.000                             | 0.000       |
| 2024 Mar          | 0.015  | 0.000  | 0.000                     | 0.000                       | 0.015                      | 0.000         | 0.000  | 6.970             | 0.000                                       | 0.000       | 0.000                             | 0.000       |
| 2024 Apr          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 May          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Jun          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Jul          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Aug          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Sep          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Oct          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Nov          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| 2024 Dec          |  |  |                           |                             |                            |               |  |                   |   |             |                                   |             |
| Total             | 0.216  | 0.000  | 0.000                     | 0.000                       | 0.216                      | 0.000         | 0.000  | 26.070            | 0.000                                       | 0.000       | 0.000                             | 0.000       |

Note:

1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.

2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.



# Appendix M

---

Cumulative Statistics on Environmental  
Complaints, Notifications of Summons and  
Successful Prosecutions

## Environmental Complaints Log

| Reference No. | Date of Complaint Received | Received From | Received By | Nature of Complaint | Date of Investigation | Outcome | Date of Reply |
|---------------|----------------------------|---------------|-------------|---------------------|-----------------------|---------|---------------|
|               |                            |               |             |                     |                       |         |               |

## Cumulative Statistics on Complaints

| Environmental Aspects | Cumulative No. Brought Forward | No. of Complaints This Month | Cumulative Project-to-Date |
|-----------------------|--------------------------------|------------------------------|----------------------------|
| Air                   | 0                              | 0                            | 0                          |
| Noise                 | 0                              | 0                            | 0                          |
| Water                 | 0                              | 0                            | 0                          |
| Waste                 | 0                              | 0                            | 0                          |
| Total                 | 0                              | 0                            | 0                          |

## Cumulative Statistics on Notification of Summons and Successful Prosecutions

| Environmental Aspects | Cumulative No. Brought Forward | No. of Notification of Summons and Prosecutions This Month | Cumulative Project-to-Date |
|-----------------------|--------------------------------|--|----------------------------|
| Air                   | 0                              | 0  | 0                          |
| Noise                 | 0                              | 0  | 0                          |
| Water                 | 0                              | 0  | 0                          |
| Waste                 | 0                              | 0  | 0                          |
| Total                 | 0                              | 0  | 0                          |

# Appendix N

---

Implementation Status of Environmental  
Mitigation Measures (Construction Phase)



## Implementation Status of Environmental Mitigation Measures (Construction Phase)

| EIA Ref. (No.) | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>   | Location & (Implementation Agent)   | Implementation Status |
|----------------|---|---|-----------------------|
| 3.7.1.1 (A1)   | <b>A) Air Quality</b>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                | Sufficient dust suppression measures as stipulated under the <i>Air Pollution Control (Construction Dust) Regulation</i> (Cap. 311R), as well as good site practices and good housekeeping of the site should be properly implemented in order to minimise the construction dust generated. These measures include the followings:: |   |                       |
|                | a) Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather;  |   | Implemented           |
|                | b) Use of frequent watering for particularly dusty construction areas and areas close to ASRs;  |   | Implemented           |
|                | c) Use of frequent watering or water sprinklers for major haul roads, material stockpiling areas and other dusty activities within the construction site;   |   | Implemented           |
|                | d) Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;  |   | Implemented           |
|                | e) Provide hoarding of not less than 2.4 m high from ground level along the site boundary except for site entrance or exit;   |   | Implemented           |
|                | f) Open temporary stockpiles should be avoided or covered. Prevent placing dusty material storage piles near ASRs;  |   | Implemented           |
|                | g) Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations;   |   | Implemented           |
|                | h) Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;   |   | Implemented           |
|                | i) Imposition of speed controls for vehicles on unpaved site roads, 8 km/hr is the recommended limit;   |   | Implemented           |
|                | j) Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs;   |   | Implemented           |
|                | k) Avoid position of material stockpiling areas, major haul roads and dusty works within the construction site close to concerned ASRs; and   |   | Implemented           |
|                | l) Avoid unnecessary exposed earth.   |   | Implemented           |
| 3.7.1.2 (A2)   | Guidelines stipulated in EPD's <i>Recommended Pollution Control Clauses for Construction Contracts</i> should be incorporated in the contract documents to abate dust impacts. The clauses include:   | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                | a) The contractor shall observe and comply with the <i>Air Pollution Control Ordinance</i> and its subsidiary regulations, particularly the <i>Air Pollution Control (Construction Dust) Regulation</i> .   |   | Implemented           |
|                | b) The contractor shall undertake at all times to prevent dust nuisance as a result of the construction activities.   |   | Implemented           |
|                | c) The contractor shall ensure that there will be adequate water supply / storage for dust suppression.   |   | Implemented           |
|                | d) The contractor shall devise, arrange methods of working and carrying out the works in such a manner so as to minimise dust impacts on the surrounding environment, and shall provide experienced personnel with suitable training to ensure that these methods are implemented.  |   | Implemented           |
|                | e) Before the commencement of any work, the contractor may require to submit the methods of working, plant, equipment and air pollution control system to be used on the site for the engineer inspection and approval.   |   | Implemented           |
| 3.4.1.4 (A3)   | <u>Control on fuel combustion from the use of PMEs</u>  | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                | a) Legal control on the types of fuel allowed for use and their sulphur contents in commercial and industrial processes should be observed.   |   | Implemented           |
|                | b) Only approved or exempted non-road mobile machinery should be allowed to be used in construction sites.  |   | Implemented           |
|                | c) All construction plants are required to use ultra-low-sulphur diesel (ULSD) (defined as diesel fuel containing not more than 0.005% sulphur by weight).  |   | Implemented           |

Note:

(1) Detailed EIA report and EM&amp;A Manual reference refer to the Appendix B of approved EM&amp;A Manual.

N/A: Not Available, N/O: Not Observed.

## Implementation Status of Environmental Mitigation Measures (Construction Phase)

| EIA Ref. (No.)                   | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>   | Location & (Implementation Agent)   | Implementation Status |
|----------------------------------|---|---|-----------------------|
|                                  | B) Noise  |   |                       |
| 4.8.1.2 (B1)                     | Good Site Practice  | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                                  | The site practices listed below should be followed during construction works:   |   |                       |
|                                  | a) Only well-maintained PME to be operated on site and should be serviced regularly during construction;  |   | Implemented           |
|                                  | b) Silencers or mufflers on construction equipment should be utilised (if appropriate) and should be properly maintained during the construction;   |   | N/A                   |
|                                  | c) Mobile plant, if any, should be sited as far away from NSRs as possible;   |   | Implemented           |
|                                  | d) Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;   |   | Implemented           |
| 4.8.1.3 – 4.8.1.4 & Table 7 (B2) | e) Plant known to emit noise strongly in one direction should, wherever possible, be orientated to direct noise away from the nearby NSRs; and  | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                                  | f) Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities   |   | Implemented           |
|                                  | Use of Quiet PME  |   |                       |
|                                  | The Contractors may adopt alternative quiet PME as long as it can be demonstrated that they would not result in construction noise impacts worse than those predicted in this EIA Report. Use of quiet plant should be made reference to the Powered Mechanical Equipment (PME) listed in the Technical Memorandum or the Quality Powered Mechanical Equipment (QPME) / other commonly used PME listed in Environmental Protection Department (EPD) web pages as far as possible which includes the Sound Power Level (SWLs) for specific quiet PME.  |   | Implemented           |
|                                  | Use of Movable Noise Barriers/Acoustic Mats   |   |                       |
|                                  | Movable noise barriers that can be placed close to the construction equipment and moved along with the PME are effective for screening noise from NSRs. A typical design which has been used locally is a wooden framed barrier with a cantilevered upper portion of superficial density no less than 10 kg/m <sup>2</sup> on a skid footing with internal sound absorptive lining. This measure is particularly effective for low level zone of NSRs. A longer cantilevered top cover would be required to achieve screening benefits at upper floors of NSRs. The Contractor shall be responsible for the design and actual position of the movable noise barriers with due consideration given to the position and size of the PME, and the requirement of intercepting the line-of-sight from the NSRs to the PME, as well as ensuring that the barriers should have no opening and gap. It is anticipated that properly designed noise barriers would achieve a 5 dB(A) reduction for mobile PME and a 10 dB(A) reduction for static PME. Acoustic mat with surface mass of not less than 7kg/m <sup>2</sup> would be used for plant items such as piling, oscillator and a 10 dB(A) noise reduction is anticipated. |   | Implemented           |
| 4.8.1.7 (B4)                     | Scheduling of Noisy Activities to outside Examination Period of HKBTS   | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                                  | To minimise the construction noise impact on HKBTS, the use of piling (oscillator) in ELS and concurrent use of concrete lorry mixer with other PMEs in steel fixing and concreting of structure should be avoided during the examination period of HKBTS.  |   | Implemented           |
|                                  | Contractor should keep close communication with the operator of HKBTS to obtain the updated schedule of examination at the time conducting of the relevant construction works.  |   | Implemented           |

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed.

## Implementation Status of Environmental Mitigation Measures (Construction Phase)

| EIA Ref. (No.)         | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>  | Location & (Implementation Agent)   | Implementation Status   |
|------------------------|--|---|---|
| 5.8.1.1 (C1)           | <u>Construction Site Runoff</u><br>Proper site management measures should be implemented to control site runoff and drainage, and thereby prevent high sediment loadings from entering nearby watercourses. The contractor should follow the practices, and be responsible for the design, construction, operation and maintenance of all the mitigation measures as specified in ProPECC PN 1/94 “ <i>Construction Site Drainage</i> ”. The design of the mitigation measures should be submitted by the contractor to the engineer for approval.<br>These mitigation measures should include the following practices:<br>a) At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities.<br>b) Sand / silt removal facilities such as sand / silt traps and sediment basins should be provided to remove sand / silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt / sand traps should be 5 minutes under maximum flow conditions.<br>c) All drainage facilities and erosion and sediment control structures should always be regularly inspected and maintained to ensure proper and efficient operation and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.<br>d) Measures should be taken to minimise the ingress of site drainage into excavations. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities.<br>e) If surface excavation works cannot be avoided during the wet season (April to October), temporarily exposed slope / soil surfaces should be covered by a tarpaulin or other means, as far as practicable, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Interception channels should be provided (e.g. along the crest / edge of the excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place to ensure that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm. Other measures that need to be implemented before, during and after rainstorms are summarised in ProPECC PN 1/94.<br>f) All vehicles and plant should be cleaned before leaving a construction site. An adequately designed and sited wheel washing facility should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.<br>g) Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented<br>Implemented<br>Implemented<br>Implemented<br>Implemented<br>Implemented<br>Implemented |
| 5.8.1.2 – 5.8.1.3 (C2) | <u>General Construction Activities</u><br>a) Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby water bodies and public drainage system.<br>b) Stockpiles of cement and other construction materials should be kept covered when not being used.<br>c) Oils and fuels should only be used and stored in designated areas, which have pollution prevention facilities.<br>d) All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Rainwater in the bunds should be cleared after each rain event. Waste oils, fuels and solvents collected within the bund should be handled and treated as chemical waste.   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented<br>Implemented<br>Implemented<br>Implemented  |
| 5.8.1.4 (C3)           | <u>Sewage Effluent</u><br>Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal of waste matter and maintenance of these facilities.   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented   |

Sai O Trunk Sewer Sewage Pumping Station

| EIA Ref. (No.) | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>  | Location & (Implementation Agent)   | Implementation Status |
|----------------|--|---|-----------------------|
|                | C) Water Quality   |   |                       |
| 5.8.1.5 (C4)   | <u>Construction Works in Close Proximity of Inland Waters</u>  | All construction sites / construction phase / upon completion of all construction activities (Contractor) | N/A                   |
|                | The practices outlined in ETWB TC (Works) No. 5/2005 “Protection of natural streams/rivers from adverse impacts arising from construction works” should be adopted where applicable to minimise the water quality impacts upon any natural streams or surface water systems. |   |                       |

Note:  
(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.  
N/A: Not Available, N/O: Not Observed.

## Implementation Status of Environmental Mitigation Measures (Construction Phase)

| EIA Ref. (No.)       | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>   | Location & (Implementation Agent)   | Implementation Status |
|----------------------|---|---|-----------------------|
|                      | D) Waste Management   |   |                       |
| 6.5.1.3 (D1)         | Good Site Practices   | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                      | Recommendations for good site practices during the construction phase include:  |   |                       |
|                      | a) Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility;  |   | Implemented           |
|                      | b) Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures;  |   | Implemented           |
|                      | c) Provision of sufficient waste reception / disposal points, and regular collection of waste;  |   | Implemented           |
|                      | d) Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;  |   | Implemented           |
|                      | e) Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;  |   | Implemented           |
|                      | f) Adoption of a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites); and   |   | Implemented           |
| 6.5.1.4 (D2)         | g) Preparation of Waste Management Plan (WMP), as part of the Environmental Management Plan (EMP).  | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                      | Waste Reduction Measures  |   |                       |
|                      | Recommendations to achieve waste reduction are discussed as follow:   |   |                       |
|                      | a) Segregate and store different types of construction related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;   |   | Implemented           |
|                      | b) Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors;   |   | Implemented           |
|                      | c) Recycle any unused chemicals or those with remaining functional capacity;  |   | Implemented           |
|                      | d) Maximise the use of reusable steel formwork to reduce the amount of C&D materials;   |   | Implemented           |
|                      | e) Adopt proper storage and site practices to minimise the potential for damage to, or contamination of construction materials;   |   | Implemented           |
| 6.5.1.6–6.5.1.7 (D3) | f) Plan the delivery and stock of construction materials carefully to minimise the amount of waste generated; and   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                      | g) Minimise over ordering and wastage through careful planning during purchasing of construction materials.   |   | Implemented           |
|                      | Reducing and Reuse of C&D Materials   |   |                       |
|                      | a) Careful design, planning together with good site management can reduce over-ordering and generation of C&D materials such as concrete, mortar and cement grouts. Formwork should be designed to minimise the use of standard wooden panels, so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse. |   | Implemented           |
| 6.5.1.8 (D4)         | b) To minimise off-site disposal of inert C&D material, the excavated inert materials with suitable characteristics / size should be reused on-site as fill material as far as practicable, such as for backfilling of the box culvert and drainage pipe works.   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                      | c) Prior to disposal of non-inert C&D materials, wood, steel and other metals should also be separated for reuse and / or recycle where practicable so as to minimise the quantity of waste to be disposed of to landfill.  |   | Implemented           |
|                      | Storage of C&D Materials  |   |                       |
|                      | Suitable areas should be designated within the works site boundaries for temporary stockpiling of C&D material. Within stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance:  |   |                       |
| 6.5.1.8 (D4)         | a) cover material during heavy rainfall;  | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                      | b) locate stockpiles to minimise potential visual impacts; and  |   | Implemented           |
|                      | c) minimise land intake of stockpile areas as far as possible.  |   | Implemented           |

## Sai O Trunk Sewer Sewage Pumping Station

| EIA Ref. (No.)            | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>  | Location & (Implementation Agent)   | Implementation Status |
|---------------------------|--|---|-----------------------|
|                           | D) Waste Management  |   |                       |
| 6.5.1.9 (D5)              | <u>Disposal of C&amp;D Materials</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                           | a) In order to monitor the disposal of C&D materials at the designated public fill reception facility and landfill and to control fly-tipping, a trip-ticket system should be included.  |   | Implemented           |
|                           | b) When disposing inert C&D materials at a public filling reception facility, the material shall only consist of soil, rock, concrete, brick, cement plaster / mortar, inert building debris, aggregates and asphalt. The material shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor. |   | Implemented           |
| 6.5.1.10 & 6.5.1.12 (D6)  | <u>Chemical Wastes</u>   | Construction and Operational Phase  |                       |
|                           | a) If chemical waste is produced at the construction site / the SPS, the contractor would be required to register with the EPD as a Chemical Waste Producer.   |   | Implemented           |
|                           | b) Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately.   |   | Implemented           |
|                           | c) Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc.  |   | Implemented           |
|                           | d) The contractor shall use a licensed collector to transport and dispose of the chemical wastes at the CWTC or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.   |   | Implemented           |
| 6.5.1.11 & Table 6.2 (D7) | <u>General Refuse</u>  | All construction sites / construction phase / upon completion of all construction activities (Contractor) |                       |
|                           | a) General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical wastes.   |   | Implemented           |
|                           | b) A reputable waste collector should be employed by the contractor to remove general refuse / screenings from the site on a regular basis to minimise odour, pest and litter impacts.   |   | Implemented           |
|                           | c) Clearly labelled recycling bins should be provided on site to encourage segregation and recycling of aluminium and plastic wastes, and wastepaper to reduce general refuse production.  |   | Implemented           |
|                           | d) The contractor should carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins should also be provided in the site as reminders. The recyclable waste materials should then be collected by reliable waste recycling agents on a regular basis.  |   | Implemented           |
|                           | e) The collected general refuse will be disposed of at NENT landfill.  |   | Implemented           |

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed.

## Implementation Status of Environmental Mitigation Measures (Construction Phase)

| EIA Ref. (No.)  | Environmental Protection Measures (Construction Phase) <sup>(1)</sup>   | Location & (Implementation Agent)   | Implementation Status |
|-----------------|---|---|-----------------------|
|                 | E) Landscape and Visual   |   |                       |
| Table 10.9 (E1) | <u>CM1 – Preservation of Trees</u>  | All construction sites / construction phase / upon completion of all construction activities (Contractor) | N/A                   |
|                 | Trees to be retained in accordance with DEVB TCW No. 4/2020 - Tree Preservation.  |   |                       |
| Table 10.9 (E2) | <u>CM2 – Compensatory Tree Planting</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | N/A                   |
|                 | Any trees to be felled under the Project shall be compensated in accordance with DEVB TCW No. 4/2020 - <i>Tree Preservation</i> .   |   |                       |
| Table 10.9 (E3) | <u>CM3 – Control of Night-time Lighting Glare</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                 | Any lighting provision of the construction works at night shall be carefully controlled to prevent light overspill to the nearby VSRs and into the sky.   |   |                       |
| Table 10.9 (E4) | <u>CM4 – Erection of Decorative Screen Hoarding</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                 | Decorative Hoarding, which is compatible with the surrounding settings, shall be erected during construction to minimise the potential landscape and visual impacts due to the construction works and activities.   |   |                       |
| Table 10.9 (E5) | <u>CM5 – Management of Construction Activities and Facilities</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | Implemented           |
|                 | The facilities and activities at works sites and areas, which include site office, temporary storage areas, temporary works etc., shall be carefully managed and controlled on the height, deposition and arrangement to minimise any potential adverse landscape and visual impacts. |   |                       |
| Table 10.9 (E6) | <u>CM6 – Reinstatement of Temporarily Disturbed Landscape Areas</u>   | All construction sites / construction phase / upon completion of all construction activities (Contractor) | N/A                   |
|                 | All hard and soft landscape areas disturbed temporarily during construction due to temporary excavations, temporary works sites and works areas shall be reinstated to equal or better quality, to the satisfaction of the relevant Government Departments.                           |   |                       |

Note:

(1) Detailed EIA report and EM&amp;A Manual reference refer to the Appendix B of approved EM&amp;A Manual.

N/A: Not Available, N/O: Not Observed

# Appendix O

---

Summary of Outstanding Issues and  
Deficiencies in the Reporting Month



### Summary of Outstanding Issues and Deficiencies in the Reporting Month

| Environmental Aspects         | Outstanding Issues | Deficiencies  |
|-------------------------------|--------------------|---|
| Air Quality                   | N/A                | Any items of deficiencies can be referred to <b>Appendix K.</b> |
| Noise                         | N/A                |   |
| Water Quality                 | N/A                |   |
| Chemical and Waste Management | N/A                |   |
| Landscape and Visual Impact   | N/A                |   |
| Permit / Licenses             | N/A                |   |
| Others                        | N/A                |   |
