

JOB No.: TCS00491/09

DSD CONTRACT No.: DC/2009/08

CONSTRUCTION OF YUEN LONG SOUTH BRANCH  
SEWERS AND EXPANSION OF HA TSUEN SEWAGE  
PUMPING STATION

THE FOURTH RESULTS OF LANDSCAPE AND VISUAL IMPACT MONITORING  
FOR MAY 2010 (NO.4)

PREPARED FOR

CHINA STATE CONSTRUCTION ENGINEERING  
(HONG KONG) COMPANY LIMITED

### Quality Index

Date	Reference No.	Prepared By	Certified By
9 Sep 2011	TCS00491/09/600/R00260v1	Wong Fu Nam (Senior Environmental Consultant)	T.W. Tam (Environmental Team Leader)




Version	Date	Description
1	9 Sep 2011	First submission

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.

安誠工程顧問有限公司  
香港灣仔  
皇后大道東183號  
合和中心47樓  
電話: (852) 2911 2233  
傳真: (852) 2805 5028

Hyder Consulting Limited  
Company Number 126012  
47th Floor, Hopewell Centre  
183 Queen's Road East  
Wan Chai, Hong Kong  
Tel: (852) 2911 2233  
Fax: (852) 2805 5028  
hyder.hk@hyderconsulting.com  
www.hyderconsulting.com



21 September 2011

**By Post**

Action-United Environmental Services &  
Consulting  
Unit A, 20/F, Gold King Industrial Building,  
35-41 Tai Lin Pai Road,  
Kwai Chung,  
New Territories,  
Hong Kong.

**Your Ref:**

**Our Ref:** EB000586-F/THW11-1671

For attention of: Mr. T. W. Tam

Dear Mr. Tam,

**Contract No.: DC/2009/08**

**Construction of Yuen Long South Branch Sewers and Expansion of Ha Tsuen Sewage  
Pumping Station**

**Monthly EM&A Report for Designated Project, Landscape and Visual Impact Sections, February  
to June 2010 – IEC Verification**

With reference to ET's captioned Landscape and Visual Impact section of monthly EM&A reports for five reporting months, February to June 2010 inclusive (ET's ref.: TCS00491/09/600/R0243v2, TCS00491/09/600/R0258v1, TCS00491/09/600/R0259v1, TCS00491/09/600/R0260v1 and TCS00491/09/600/R0261v1, all dated 9 September 2011) received on 16 September 2011, we have no comment and hereby verify the captioned Landscape and Visual Impact section of monthly EM&A reports.

Should there be any queries, please feel free to contact our William Law on 2911 2511.

Yours sincerely

F.C. TSANG  
Independent Environmental Checker  
HYDER CONSULTING LIMITED

FCTWL/my

**TABLE OF CONTENTS**

<b>1. INTRODUCTION</b>	<b>1</b>
<b>2. CONTENT OF THE LVIM RESULTS</b>	<b>1</b>

**APPENDIX A SITE INSPECTION CHECKLIST**

## 1. INTRODUCTION

- 1.01 This Results of Landscape and Visual Impact Monitoring (hereinafter “the LVIM Results”) is part of the monthly EM&A report under DSD Contract No.: DC/2009/08 Construction of Yuen Long South Branch Sewers and Expansion of Ha Tsuen Sewage Pumping Station: *Results of Landscape and Visual Impact* of Chapter 4 *Impact Monitoring Results*. The LVIM Results should therefore be read in conjunction with the corresponding monthly EM&A reports.
- 1.02 Pursuant to Chapter 6 *Landscape and Visual* of the EM&A Manual, EM&A for landscape and visual resources is considered to be a key aspect during both the construction and operational phases of the Project. The implementation and maintenance of landscape compensatory planting measures should therefore be checked to ensure that they are fully realized and that potential conflicts between the proposed landscape measures and any other project works and operational requirements are resolved at the earliest possible date and without compromise to the intention of the mitigation measures.
- 1.03 Monitoring of the recommended implementation of the mitigation measures is required to be conducted throughout the construction phase of the Project.
- 1.04 As a member of the ET, the landscape architect is responsible for the implementation of landscape construction works and subsequent maintenance operations during the 12 month establishment period. The establishment works should be undertaken throughout the Contractor's one year maintenance period which will be within the first operational year of the Project.
- 1.05 All measures undertaken by both the Contractor and the Landscape Contractor during the construction phase and first year of the operational phase should be audited by the landscape architect on a regular basis to ensure compliance with the intended aims of the measures.
- 1.06 Site inspections should be undertaken at least once every two weeks throughout the construction period and once every two months during the operational phase.
- 1.07 The LVIM Results has been prepared by the landscape architect and compiled by the ET upon receipt for submission to EPD after verification by the IEC.
- 1.08 To cater to closer compliance of the EM&A reporting with the EP requirements, it has been agreed among the RE, IEC and ET that The LVIM Results is submitted separately as a stand-alone submission.
- 1.09 This is the fourth (No. 4) LVIM Results, covering the construction period from 1 to 30 May 2010 (hereinafter “the Result Period”).

## CONTENT OF THE LVIM RESULTS

- 2.01 This LVIM Results contains the site inspection checklist for the Result Period, where landscape and visual impact monitoring results are presented and where necessary, the associated recommendations are included.
- 2.02 The site inspection checklist is enclosed in **Appendix A**.

## **Appendix A**

### **Site Inspection Checklist**

## Landscape and Visual Impact Assessment Site Inspection Checklist

**Contract No.:** DC/2009/08  
**Contract title:** Construction of Yuen Long South Sewer and Expansion of Ha Tsuen Sewage Pumping Station  
**Contractor:** China State Construction Engrg. (HK) Ltd.  
**Location:** Ha Tsuen Sewage Pumping Station  
**Inspection Date:** 13-May-2010

		Satisfactory			Rectified		Remarks
		N/A	Yes	No	Yes	No	
<b>I. General</b>							
1.	Erect hoarding around site boundary properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<hr/>
2.	Keep well maintenance of hoarding	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<hr/>
3.	All construction works are carried out within site boundary properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<hr/>
4.	Carry out the initial tree survey prior to construction	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<hr/>
5.	Provide tree labels according to tree survey records	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<hr/>

Comments:

Standard hoarding was erected and well maintained around the works area at Ha Tsuen Sewage Pumping Station (HTSPS).

All trees were labelled as requirement.

### II. Transplanting Works

1. All transplanting works are carried out in accordance with the specifications	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. The transplanted trees are kept in regular inspection within the establishment period	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Item 1
3. The transplanted trees are kept in maintenance throughout the establishment period as follows:						
(i) Watering	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ii) Weeding	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iii) Fertilising	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iv) Littering	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(v) Grass cutting	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vi) Firming up	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vii) Pest control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(viii) Disease control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ix) Pruning	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(x) Replacement	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

There had total 73 nos. of transplanted trees in Ha Tsuen Sewage Pumping Station due to construction works under this contract.

Watering and weeding should be undertaken periodically.

### III. Landscaping Works

1. All landscaping works are carried out in accordance with the specifications	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. The landscaping plants are kept in regular inspection within the establishment period	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

## Landscape and Visual Impact Assessment Site Inspection Checklist

	Satisfactory			Rectified		Remarks
	N/A	Yes	No	Yes	No	
3. The landscaping plants are kept in maintenance throughout the establishment period as follows:						
(i) Watering	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ii) Weeding	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iii) Fertilising	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iv) Littering	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(v) Grass cutting	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vi) Firming up	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vii) Pest control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(viii) Disease control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ix) Pruning	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(x) Replacement	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

No landscaping works were carried out in the reporting month

### IV. Preservation and Protection of Trees

1. All preserved trees are protected in accordance with the specifications	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. All preserved trees are fenced off properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. No construction activities are carried out in the protection zone of the preserved trees	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

All retained trees were fenced off and protected properly within the works area of the site.

Keep in review of the piling works with the impacts on the retained trees within the works area.

### Conclusion


Generally, the overall are normal in the transplanting and visual impact at Ha Tsuen Sewage Pumping Station. The conditions of hoarding was satisfactory. The protection works maintained for the transplanted and the preserved trees. The health conditions of some transplanted trees should be reviewed in the regular inspection as per attached. More Frequently watering is required

### Remarks

- The regular inspection for the transplanted trees was scheduled at the end of the reporting month.

Signatures:

Senior Landscape Architect

  
(Name: David Bloxham CMLI UK )

**Contract No.:** DC/2009/08  
**Contract title:** Construction of Yuen Long South Sewer and Expansion of Ha Tsuen Sewage Pumping Station  
**Contractor:** China State Construction Engrg. (HK) Ltd.  
**Location:** Ha Tsuen Sewage Pumping Station  
**Inspection Date:** 24-May-2010

		Satisfactory			Rectified		Remarks
		N/A	Yes	No	Yes	No	
<b>I. General</b>							
1.	Erect hoarding around site boundary properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.	Keep well maintenance of hoarding	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.	All construction works are carried out within site boundary properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.	Carry out the initial tree survey prior to construction	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.	Provide tree labels according to tree survey records	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

Standard hoarding was erected and well maintained around the works area at Ha Tsuen Sewage Pumping Station (HTSPS).

The construction has no implication to protected tree. Close monitoring the implication of piling works to protected tree is required

## II. Transplanting Works

1. All transplanting works are carried out in accordance with the specifications	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. The transplanted trees are kept in regular inspection within the establishment period	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Item 1
3. The transplanted trees are kept in maintenance throughout the establishment period as follows:						
(i) Watering	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ii) Weeding	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iii) Fertilising	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iv) Littering	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(v) Grass cutting	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vi) Firming up	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vii) Pest control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(viii) Disease control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ix) Pruning	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(x) Replacement	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

There had total 73 nos. of transplanted trees in Ha Tsuen Sewage Pumping Station due to construction works under this contract.

Watering should be undertaken periodically. More pruning for die branch is required

## III. Landscaping Works

1. All landscaping works are carried out in accordance with the specifications	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. The landscaping plants are kept in regular inspection within the establishment period	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	Satisfactory			Rectified		Remarks
	N/A	Yes	No	Yes	No	
3. The landscaping plants are kept in maintenance throughout the establishment period as follows:						
(i) Watering	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ii) Weeding	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iii) Fertilising	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(iv) Littering	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(v) Grass cutting	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vi) Firming up	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(vii) Pest control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(viii) Disease control	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(ix) Pruning	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
(x) Replacement	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

No landscaping works were carried out in the reporting month

#### IV. Preservation and Protection of Trees

1. All preserved trees are protected in accordance with the specifications	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. All preserved trees are fenced off properly	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. No construction activities are carried out in the protection zone of the preserved trees	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Comments:

All retained trees were fenced off and protected properly within the works area of the site.

#### Conclusion

Generally, the overall conditions are normal in the transplanting and visual impact at Ha Tsuen Sewage Pumping Station. The conditions of hoarding was satisfactory. The protection works maintained for the transplanted and the preserved trees. The health conditions of the transplanted trees should be reviewed in the regular inspection in the establishment period. Some of the die branch need to remove and frequency watering is required

#### Remarks

- The regular inspection for the transplanted trees was scheduled at the end of the reporting month.

Tree Nos.	Health	Tree Form	Comments	Suggested treatment
D1231	Fair	Fair	Found parasitic plants	Remove the parasitic plants
D1233	Fair	Fair	The aerial root were knot	Release the knot
D1240	Fair	Fair	Die branch	Pruning the dead branch
D1245	Fair	Fair	Found parasitic plants	Remove the parasitic plants

Signatures:

Senior Landscape Architect

  
(Name: David Bloxham CMLI UK )



D1233



D1231






D1245



D1240





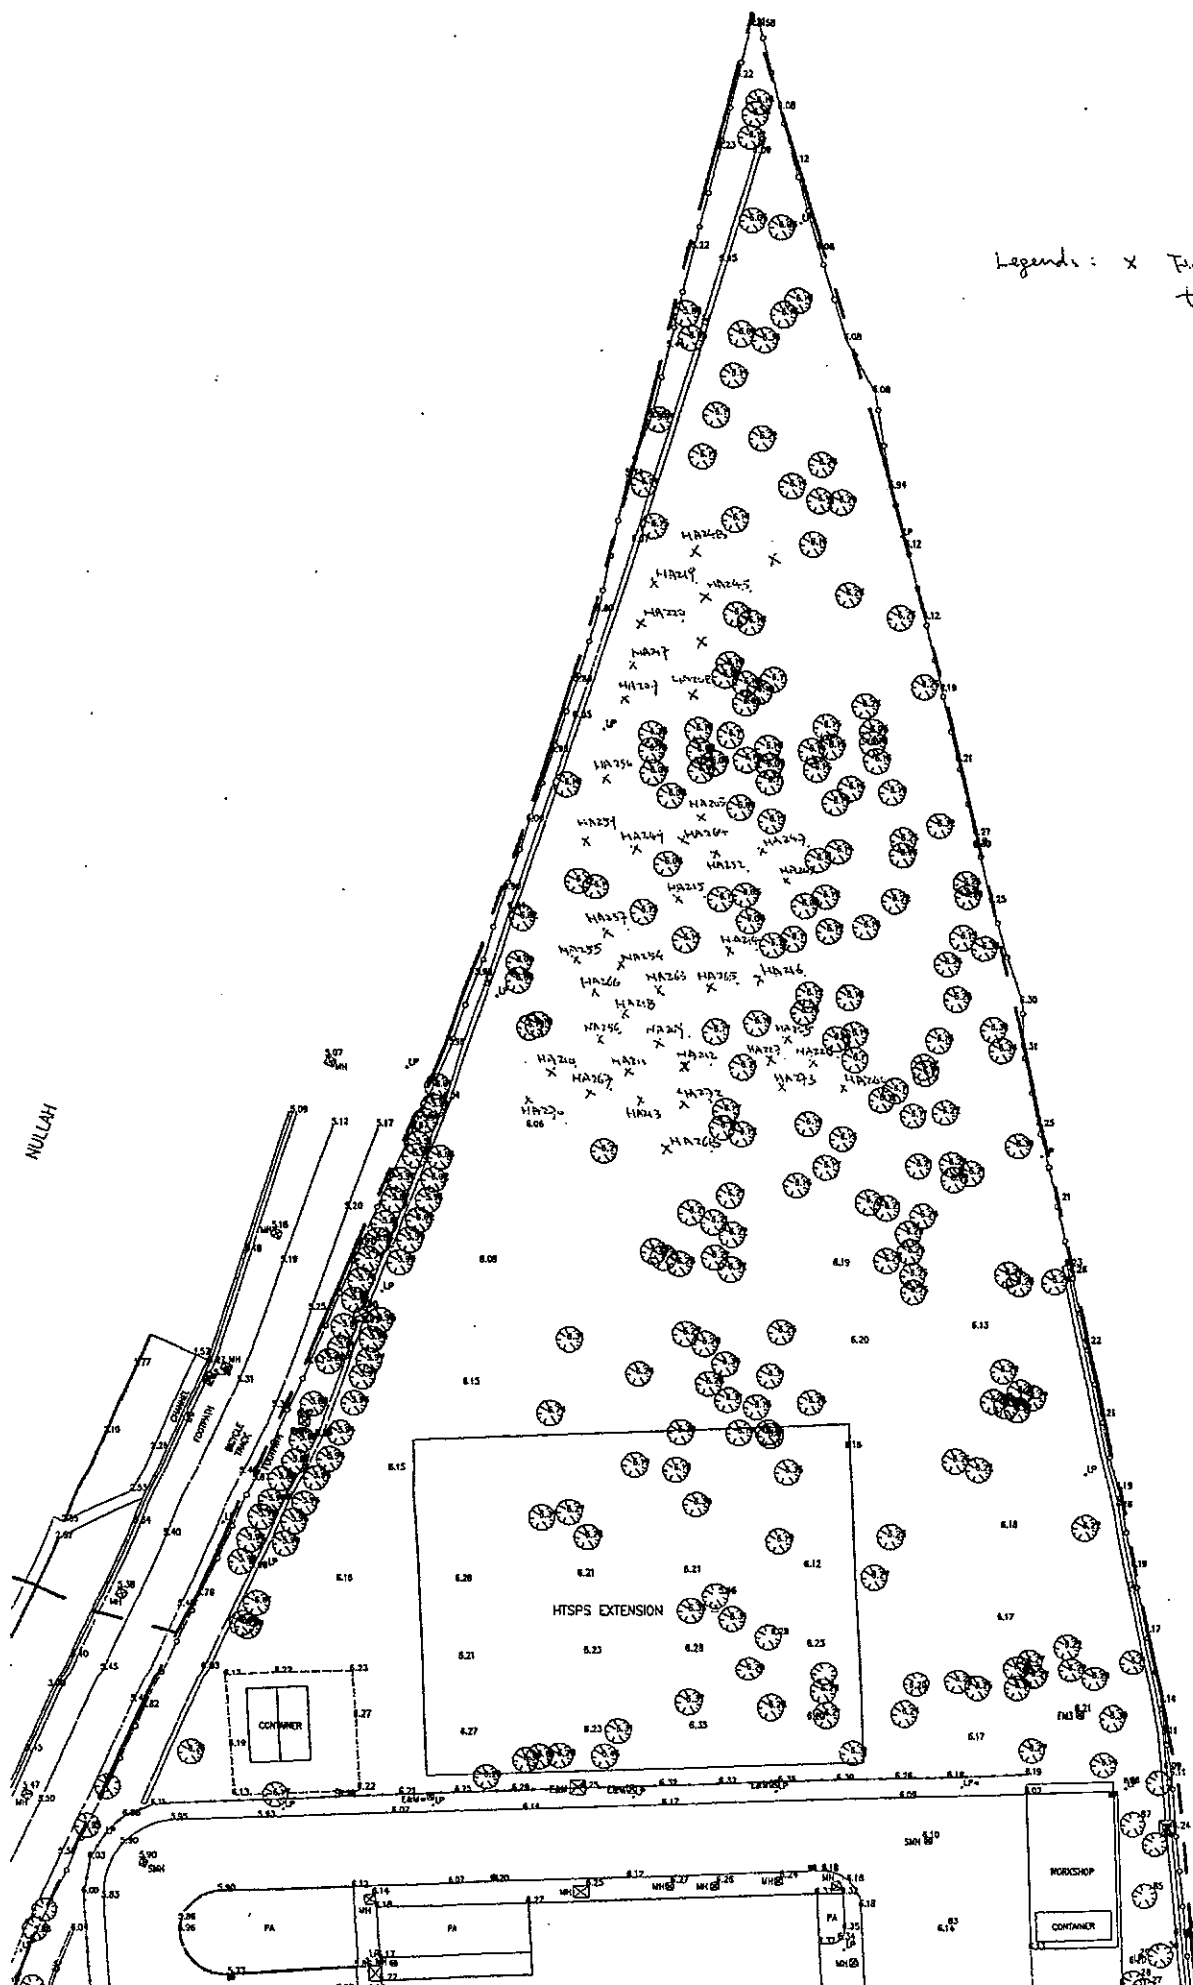

Legend: X Final location of tree transplant

