

BARBICAN CONSTRUCTION CO., LTD

**Contract No. HY/2001/18
Sai Sha Road Widening between Kam Ying
Road and Future Trunk Road T7 Junction**

**MONTHLY ENVIRONMENTAL MONITORING
& AUDIT REPORT
REPORT NO. 10**

Document No. R/2563/014 Issue 1

August 2003

Babtie Asia





Babtie Asia

R/2563/014
Issue 1
August 2003

Contract No. HY/2001/18
Sai Sha Road Widening between Kam Ying Road and
Proposed Road T7 Junction

Monthly Environmental Monitoring & Audit Report
Report No. 10

Approved for Issue by:  ----- Mr Mark Cheung (Babtie Asia Ltd.) Position: Environmental Team Leader Date: 4 August 2003
Verified by:  ----- Ms. Lyn Ip (BMT Asia Pacific Limited) Independent Position: Environmental Checker Date: 11 AUGUST 2003

Barbican Construction Co. Ltd
G/F Shop 11 & 1st Floor,
2 Landale Street,
Wanchai
HONG KONG

Babtie Asia
15/F, Cornwall House
Taikoo Place, 979 King's Road
Quarry Bay
HONG KONG

CONTRACT NO. HY/2001/18
SAI SHA ROAD WIDENING BETWEEN KAM YING ROAD
AND FUTURE TRUNK ROAD T7 JUNCTION

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

REPORT NO. 10

CONTENTS

EXECUTIVE SUMMARY

1.0 ENVIRONMENTAL STATUS

- 1.1 Background
- 1.2 Contact Details of Key Personnel
- 1.3 Construction Programme
- 1.4 Site Management Structure
- 1.5 Works Undertaken during the reporting period with Illustrations
- 1.6 Project Area, Sensitive Receivers & Monitoring Locations

2.0 IMPLEMENTATION STATUS

- 2.1 Advice on the Implementation Status of Environmental Protection & Pollution Control / Mitigation Measures
 - 2.1.1 Construction Noise Mitigation Measures
 - 2.1.2 Landscape and Visual Mitigation Measures

3.0 MONITORING RESULTS

- 3.1 Graphical Plots of the Monitored Parameters
- 3.2 Major Activities During the Reporting Period
- 3.3 Noise Monitoring Methodology
- 3.4 Noise Monitoring Equipment
- 3.5 Calibration Details
- 3.6 Noise Parameters
- 3.7 Monitoring Locations
- 3.8 Monitoring Date, Time, Frequency and Duration
- 3.9 Noise Monitoring Results
- 3.10 Weather Conditions
- 3.11 Influencing Factors
- 3.12 QA/QC Results and Detection Limits

4.0 RECORD OF NON-COMPLIANCE OF THE ACTION AND LIMIT LEVELS, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

- 4.1 Non-compliance of the Action and Limit Levels
 - 4.1.1 Noise
- 4.2 Written Complaints and Verbal Complaints

4.3 Notifications of Summons and Successful Prosecutions

5.0 OTHERS

5.1 Future Key Issues

5.2 Advice on the Solid and Liquid Waster Management Status

5.2.1 General Refuse

5.2.2 Liquid Waste Management

APPENDICES

Appendix A Construction Programme

Appendix B Site Organization Chart

Appendix C Record Photos for Construction works taken in July 2003

Appendix D The Project Area, Environmental Sensitive Receivers and the Locations of the Monitoring Stations

Appendix E Calibration Certificates for Sound Level Meter

Appendix F Data of Noise Monitoring

Appendix G Graphical Representation of Construction Noise Monitoring Data

Appendix H Weather Conditions during the Monitoring Period

Appendix I Impact Noise Monitoring Limit Action Level

Appendix J Graphical Plots of Trends of Monitored Parameters

Appendix K Construction Noise Monitoring and Site Audit Schedules
July 2003 and August 2003

Appendix L Statistics for Environmental Complaints

EXECUTIVE SUMMARY

This is the tenth EM & A Report for the project of Sai Sha Road Widening between Kam Ying Road and Future Trunk Road T7 Junction.

This report mainly presents the EM & A works undertaken for the above project from 1 July 2003 to 31 July 2003 in accordance with the EM & A Manual under Appendix H.3 of the Particular Specification.

Noise Level

L_{eq} (30min) noise level measurement was performed at CNM 1, CNM 2 and CNM 3. CNM 1 is for noise sensitive receivers (NSRs 1 & 2) Wu Kwai Sha New Village. CNM 2 is for (NSRs 3 & 4) Kam Lung Court/ Lee On Estate. CNM 3 is for (NSR7) Residential Development at Wu Kai Sha DD 206. The limit level for all the noise sensitive receivers is 75 dB(A).

The construction noise monitoring was taken on the 3rd, 10th, 17th and 25th of July 2003. All the measured noise levels at three monitoring stations are below the noise limit level.

Complaint log

No written or verbal complaints were received during the reporting period.

Others

No notifications of summons, no successful prosecutions were received during the reporting period.

Future Key Issues

Adverse influence on both air quality and noise level is anticipated from future construction activities, such as mini pile works for the footbridge construction and the machine operation on the unpaved haul road near Kam Lung Court and Lee Wing House. The Contractor should carry out good site practice to minimise the potential air pollution and noise pollution.

The site runoff resulting from the pile works for the construction of footbridges should be properly treated before being discharged to the stormwater drainage system.

The Contractor should exert himself to eliminate the presence of accumulation of stagnant water to avoid the breeding of mosquitoes and the spread of dengue fever.

To improve the hygiene condition of the site, the Contractor should regularly remove the rubbish within the site area and provide rubbish bins as far as possible.

The proposal of suspension of noise monitoring works at the location of the CNM 3 was agreed by the Department of Environmental Protection. The noise monitoring works at CNM3 will be suspended with effect in August 2003. In case there is any new noise sensitive receiver(s) established at the site of Wu Kwai Sha DD 206 during the remaining construction period, the monitoring work will be immediately resumed and conducted in accordance with the requirements set out in the Environmental Monitoring and Audit Manual.

1.0 ENVIRONMENTAL STATUS

1.1 Background

Babtie Asia Ltd was employed by the Contractor to act as the Environmental Team for this project. The Independent Environmental Checker is BMT Asia Pacific Limited.

The purpose of this document is to report the Environmental Monitoring & Audit (EM & A) works in the period between 1 July 2003 and 31 July 2003.

1.2 Contact Details of Key Personnel

Titles, names and contact telephone numbers of the key personnel of the captioned project are tabulated below:

Title	Name	Contact Number
Engineer's Representative (Highways Department)	Mr. Greg Leung	2716 1043
EPD	Mr. Simon Hui	2835 1105
Project Director (Contractor)	Mr. David Kong	2137 5522
Project Manager (Contractor)	Mr. Alan Tam	9161 2991
Site Agent (Contractor)	Mr. K I Mok	9813 9599
Environmental Team Leader (Babtie Asia Limited)	Mr. Mark Cheung	2738 3803
Independent Environmental Checker (BMT Asia Pacific Limited)	Ms. Lyn Ip	2241 9812

1.3 Construction Programme

The latest construction programme is attached in Appendix A. This construction programme is subject to continuous refinement.

1.4 Site Management Structure

The site organization chart is shown as Appendix B.

1.5 Works undertaken during the reporting period with illustrations

The works for this project are divided into three sections: Section 1, Section 2 and Section 3.

Section 1 comprises all the works for the completion of the subway system connecting the existing vacant subway barrel across Sai Sha Road adjacent to Kam Ying Road and the local widening of northern Kam Ying Road and all associated landscaping works.

Section 2 comprises all construction works including the new carriageways, two footbridges and all footpath, cycle tracks, subways, village access road, noise barriers, roundabout and associated works comprising drainage works, E&M works, traffic signs and aids, slope works, embankments, retaining walls, subway wing walls, cycle parks, fencing, street lighting and all associated landscaping works, except Section 1 and Section 3.

Section 3 comprises all the works for the new access road to Whitehead and all the works except Section 1 and 2.

The works undertaken during the reporting period were as follows:

- Drainage Works - Manhole and drainage pipes construction at the area adjacent to the Wu Kai Sha Railway Station.
- Construction of Subway (P8F) – Concrete wall, base slab and staircase roof construction
- Construction of Subway (S1) – Subbase construction for Ramp 1 & Ramp 2
- Construction of Subway (S2) – Top slab and wall construction of the main barrel
- Construction of Footbridge No.1 (FB1) near Lee Wing House of Lee On Estate and near Wu Kwai Sha New Village – Excavation for construction of southern pile cap; Minipile drilling for northern pile cap; trial pit for both north and south noise barrier
- Construction of retaining wall 1 – Construction of footing

The photos showing the construction works in the reporting period are shown in Appendix C.

1.6 Project Area, Sensitive Receivers & Monitoring Locations

The drawings showing the project area, noise sensitive receivers (NSRs) and the locations of the monitoring stations are shown in Appendix D.

The construction noise monitoring stations are CNM 1, CNM 2 and CNM 3.

CNM 1 is for noise sensitive receivers (NSRs 1 & 2) Wu Kwai Sha New Village. CNM 2 is for (NSRs 3 & 4) Kam Lung Court/ Lee On Estate. CNM 3 is for (NSR7) Residential Development at Wu Kai Sha DD 206.

It is noted that the locations of the monitoring stations are the same as those adopted in the Noise Baseline Monitoring.

2.0 IMPLEMENTATION STATUS

According to the EIA report, the following should be implemented for the fourth construction phase quarter.

Location	Reference Section	Environmental Protection Measures	Agent
<i>Construction Noise Mitigation</i>			
Wu Kwai Sha New Village (1)	EIA 3.5.25	Mitigation Option 2	Contractor
Wu Kwai Sha New Village (2)	EIA 3.5.23	Mitigation Option 2	Contractor
Lok Wo Sha (1)	EIA 3.5.23	Mitigation Option 1	Contractor
Lok Wo Sha (2)	EIA 3.5.23	Mitigation Option 2	Contractor
Kam Lung Court (1)	EIA 3.5.25	Mitigation Option 2	Contractor
Kam Lung Court (2)	EIA 3.5.25	Mitigation Option 2	Contractor
Lee On Estate (1)	EIA 3.5.25	Mitigation Option 2	Contractor
Lee On Estate (2)	EIA 3.5.25	Mitigation Option 2	Contractor
Residential Development STTL446	EIA 3.5.23	Mitigation Option 1	Contractor
Residential Development at Wu Kai Sha DD206	EIA 3.5.23	Mitigation Option 1	Contractor

- Note: The locations of the noise assessment points are shown in the Figure 7 of the EIA Report.

Location	Reference Section	Environmental Protection Measures	Agent
<i>Landscape and Visual Mitigation Measures for the Construction Phase</i>			
All Scheme Roads	EIA 4.5.1	<ul style="list-style-type: none"> • Conservation of topsoil; • Screening of site construction works by use of hoardings; • Surface treatment of site hoardings to enhance visual interest and harmony with surrounding landscape / townscape; • Locating site offices and other temporary buildings in least visually prominent locations; • Efficient programming of construction works to reduce duration of construction works; • Staging of construction works to minimise areas requiring site hoardings which creates visual intrusion; • Re-routing of pedestrian routes away from the work site where possible; • Retaining existing trees and minimising damage to vegetation where possible. Care shall be taken not to damage those trees identified in the Tree Survey Report to be retained during the construction phase; and • Careful and efficient transplanting of existing vegetation carried out under the supervision of a professional landscape architect 	Contractor

2.1 Advice on the Implementation Status of Environmental Protection & Pollution Control / Mitigation Measures

2.1.1 Construction Noise Mitigation Measures

The Contractor should use silencers or mufflers on construction equipment such as pneumatic breaker and air compressor to avoid exceeding the noise limit level and annoyance to the nearby sensitive receivers.

Regular maintenance of the construction plant is strongly encouraged to avoid black smoke and excessive noise production. The machines and plant should be shut down or throttled down to a minimum when they are in intermittent use.

The plant known to emit noise strongly in one direction should be orientated to direct noise away from nearby noise sensitive receivers. The mobile plants should be sited as far away from the noise sensitive receivers as possible.

Care should be taken that different mitigation plans (option 1 & option 2) will be applied to different noise sensitive receivers. For mitigation option 2, more stringent environmental control will be required and implemented. The Contractor should pay particular attention to follow and carry out the mitigation measures mentioned in the EIA Report for those sensitive receivers to whom mitigation option 2 should be applied.

It is noted that for different construction phase quarters, the mitigation option will be different. The detailed environmental mitigation implementation schedule is shown in the EIA Report Annex A for different construction phases.

2.1.2 Landscape and Visual Mitigation Measures

Care should be taken not to damage those trees identified in the Tree Survey Report to be retained during the construction phase.

In case of the conflict between the construction machine and the trees during the construction activities, the Contractor may consider adopting an alternative construction approach to protect the trees from being damaged. As the last resort, the tree transplanting method may be considered. However, prior to such action, approval from the Engineer, the Environmental Team Leader and the Independent Environmental Checker should be obtained.

Whenever tree transplanting is required, the Contractor should notify the ET in advance and should carry out the works under the supervision of a professional landscape architect as stipulated in the EM & A Manual.

3.0 MONITORING RESULTS

3.1 Graphical plots of the monitored parameters

The graphical presentations of the monitored parameters during the reporting period are shown in Appendix G.

3.2 Major Activities During the Reporting Period

Major activities during July 2003 include the followings:

- Drainage Works - Manhole and drainage pipes construction at the area adjacent to the Wu Kai Sha Railway Station.
- Construction of Subway (P8F) – Concrete wall, base slab and staircase roof construction
- Construction of Subway (S1) – Subbase construction for Ramp 1 & Ramp 2
- Construction of Subway (S2) – Top slab and wall construction of the main barrel
- Construction of Footbridge No.1 (FB1) near Lee Wing House of Lee On Estate and near Wu Kwai Sha New Village – Excavation for construction of southern pile cap; Minipile drilling for northern pile cap; trial pit for both north and south noise barrier
- Construction of retaining wall 1 – Construction of footing

3.3 Noise Monitoring Methodology

Construction noise monitoring was carried out by using a Sound Level Meter to ensure that exceedance in noise levels could be readily identified and timely action taken to reduce the noise levels to within allowable limits.

3.4 Noise Monitoring Equipment

The approved integrating Sound Level Meter, Model No. CESVA SC20-e, in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specification as referred to in the Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO), was used for construction noise measurement.

3.5 Calibration Details

A sound level calibrator, Model No. CESVA CB-5, was used to calibrate the Sound Level Meter before and after the measurement on site.

A copy of calibration certificates conducted by DICESVA S.L. for the Sound Level Meter and the Sound Calibrator is attached in Appendix E.

3.6 Noise Parameters

The construction noise levels were measured in terms of equivalent A-weighted sound pressure level (L_{eq}) measured in decibels (dB).

$L_{eq(30min)}$ was used as the monitoring parameter for the time period between (0700 to 1900) hours on normal weekdays.

$L_{eq(5min)}$ was used as the monitoring parameter for all other time period, if applicable.

The two statistical sound levels L_{A10} and L_{A90} , the level exceeded for 10 and 90 percent of the measurement time respectively, were also recorded as supplementary information for reference.

The construction noise monitoring limit and action level is shown in Appendix I.

3.7 Monitoring Locations

The construction noise monitoring was conducted at three noise sensitive receivers, namely, CNM 1 (Wu Kwai Sha New Village), CNM 2 (Kam Lung Court/ Lee On Estate) and CNM 3 (Residential Development at Wu Kai Sha DD 206).

Both the measurement points for CNM 1 and CNM 2 are at facade while the measurement for CNM 3 is under free field measurement. Hence, a correction of + 3 dB(A) will be made to the data for CNM 3.

Locations of construction noise monitoring stations and photos are shown in Appendix D.

3.8 Monitoring Date, Time, Frequency and Duration

The monitoring frequency will depend on the scale of the construction activities. The following was adopted as an initial arrangement of measurement on the regular monitoring frequency for each station on a per week basis when noise generating activities are underway:

- (a) one set of measurements between 0700 – 1900 hours on normal weekdays;
- (b) one set of measurements between 1900 – 2300 hours;
- (c) one set of measurements between 2300 – 0700 hours; and
- (d) one set of measurements between 0700 – 1900 hours on holidays

During the reporting period, the construction noise monitoring was conducted on 3rd, 10th, 17th and 25th July and followed the scheme (a). The time and duration of measurement are shown in the Appendix F. The construction noise monitoring schedule for July 2003 and August 2003 is shown in Appendix K.

3.9 Noise Monitoring Results

The data for noise monitoring is presented in Appendix F. Graphical representation of construction noise monitoring data is presented in Appendix G.

For CNM 1, the results show that during the reporting period, the noise level is in average 64.5 dB(A) which is below the noise limit level 75 dB(A).

For CNM 2, the results show that during the reporting period, the noise level is in average 67.2 dB(A) which is below the noise limit level 75 dB(A).

For CNM 3, the results show that during the reporting period, the noise level is in average 69.2 dB(A) which is below the noise limit level 75 dB(A).

The major noise sources during the reporting period include the machines operation such as backhoe, mini pile works for footbridge (FB 1) near Lee Wing House and Wu Kwai Sha New Village, and the traffic of the heavy vehicles like trucks and buses along the Sai Sha Road. Other noise source includes residential noise.

3.10 Weather Conditions

The weather conditions were mainly sunny and did not affect the environmental monitoring works during the reporting period. The weather conditions during the period are shown in the Appendix H.

3.11 Influencing Factors

The construction of the KCRC Wu Kai Sha Station and construction of the public transport interchange and the associated development is being undertaken near the noise monitoring station CNM 3. These will contribute to the generation of noise production affecting CNM 3.

The construction works of the ASD site area near Lee On Estate slightly affected the noise monitoring results especially for CNM 2. The traffic noise from Sai Sha Road significantly contributed to the noise pollution.

3.12 QA/QC Results and Detection Limits

The QC result is shown in Appendix E. The lower limit of the sound level meter for L_{eq} is 0 dB(A). The upper limit for L_{eq} is 137 dB(A).

4.0 RECORD OF NON-COMPLIANCE OF THE ACTION AND LIMIT LEVELS, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

4.1 Non-compliance of the Action and Limit Levels

4.1.1 Noise

During the reporting period, the noise levels for all three monitoring stations (CNM 1, CNM 2 and CNM 3) were within the noise limit level.

No non-compliance of noise level was recorded.

4.2 Written Complaints and Verbal Complaints

No written and verbal complaints were received during the reporting period.

The following table shows the summary for all the complaints received since the commencement of the Contract.

TOTAL NO. OF COMPLAINT	NO. OF COMPLAINT RECEIVED WITHIN REPORTING PERIOD	NO. OF COMPLAINT THAT IS STILL UNDER INVESTIGATION	NO. OF CLOSED COMPLAINT
1	0	0	1

The statistics for environmental complaint is shown in Appendix L.

4.3 Notifications of Summons and Successful Prosecutions

No notifications of summons or successful prosecutions were received by the Contractor regarding the non-compliance of the environmental performance of the construction site during the reporting period.

5.0 OTHERS

5.1 Future Key Issue

In the coming month, the following activities will be undertaken.

- the construction of subways
- the construction of mini piles for the footbridge
- the construction of pile cap for the footbridge
- the construction of drainage works
- machines operation on unpaved haul road

Potential environmental impacts due to the above construction works are associated with dust, noise and site runoff.

The locations of the undertaking mini pile works for the footbridge are very near to the Kam Lung Court, Lee On Estate and Wu Kwai Sha New Village. Since these three sensitive receivers should be protected by the noise mitigation option 2 under the EIA Report, the Contractor should minimise the noise pollution resulting from the operation of the machines and plant.

In addition, the Contractor should strengthen the protective measures for pedestrians from being splashed on with muddy water or grout resulting from the mini pile works for footbridge construction near Lee Wing House of Lee On Estate and near the Wu Kwai Sha New Village. Close monitoring on these two locations should be carried out to avoid the complaint from the residents.

Since the heavy rainstorm season is coming, the Contractor should clean the sediments which block the stormwater U-channels within the site area. The Contractor should also remove any rubbish within the site area. In addition, the Contractor should exert himself to eliminate the presence of accumulation of stagnant water to avoid the breeding of mosquitoes and the spread of dengue fever.

Nonetheless, with the implementation of the following mitigation measures, potential impacts to the surrounding sensitive receivers could be minimised.

Construction Dust

- Regular watering of unpaved areas and the dry topsoil
- Regular watering during the demolition works such as the breaking of rigid pavement
- Cover the stockpiles with tarpaulin
- Investigate other dust sources
- Maintain onsite machinery and vehicles regularly
- Limit the speed of construction vehicles

Construction Noise

- Carry out good site practice
- Use quieter plant
- Adopt quiet working methods

- Enclose certain type of power mechanical equipment such as generators and compressors.
- Shut down the machines and plant that may be in intermittent use between work periods or throttled them down to a minimum.
- Provide temporary movable vertical barrier

Construction Site Runoff

- Direct the site runoff to the desilting facilities
- Desilt the site runoff before discharging it into the stormwater system.

5.2 Advice on the solid and liquid waste management status

5.2.1 General Refuse

General refuse may be generated by site workers. Bins shall be provided for containment prior to disposal of such waste. The Contractor should avoid the accumulation of waste materials or rubbish on site.

If there is any chemical waste or oil generated by the site, they should be properly treated and disposed of as chemical waste. If applicable, the Contractor should register as a chemical waste producer under the registration of the Department of Environmental Protection.

Environmental awareness shall be encouraged in office so as to reduce volume of office waste.

5.2.2 Liquid Waste Management

The accumulation of stagnant water within the construction site should be avoided to eliminate breeding grounds of mosquitoes.

To achieve this, the Contractor should identify potential stagnant areas on the Site and take necessary rectification action, provide personnel to inspect the Site and take appropriate action to ensure no mosquitoes can breed.

Sprinkling the Larvicidal Oil is regarded as the short term measure before the stagnant water is discharged. However, discharging the stagnant water should be the solution for long term.

To control the silty water, the Contractor should provide sandbags/ bunds to direct site surface runoff to the desilting facilities such as sedimentation tanks. The desilting facilities should be properly operated and maintained. In the meantime, the sedimentation tank should not become a pool of stagnant water to avoid the breeding of mosquitoes and other insects. Care should also be taken to ensure the capacity of the desilting facilities is sufficient to handle the discharge and to avoid overflow of the silty water.

The desilting facilities should be maintained properly. Regular removal of the accumulated debris with proper disposal is recommended.

For the wastewater generated from the site area, the Contractor should identify the sources. The produced wastewater should be collected and treated prior to disposal.

5.3 Suspension of Noise Monitoring Work at CNM 3 in Construction Phase

As mentioned in the Quarterly EM & A Report No.03, after the ET Leader had reviewed the current site situation, it was found that there were no sensitive receivers near the monitoring station CNM 3. The area delineated for Residential Development at Wu Kai Sha DD 206 is still an open car park. The noise monitoring work at that location is therefore considered to be unnecessary.

In view of this, the ET Leader notified all concerned parties including the Contractor, the IEC, the Engineer's Representative and the EPD's officials concerning the proposal of suspending noise monitoring works at the location of CNM 3 during the construction phase. Since the ET Leader received no objection from all parties, the suspension of noise monitoring works at this location will be in effect starting in August 2003.

However, in case there are any new noise sensitive receivers established at the site of Wu Kai Sha DD 206 during the remaining construction period, noise monitoring works at that location will be immediately resumed and conducted in accordance with the requirements set out in the Environmental Monitoring and Audit Manual.




APPENDIX A
CONSTRUCTION PROGRAMME

Barbican Construction Limited
 Central Plot, H302801/18
 Sai Sha Road Widening Between Kwan Ming Road and Futuro Trunk Road T7 Junction


Detailed Working Programme for Completion of Section 2 Works

Date: 28 May 2020


Rev: 3

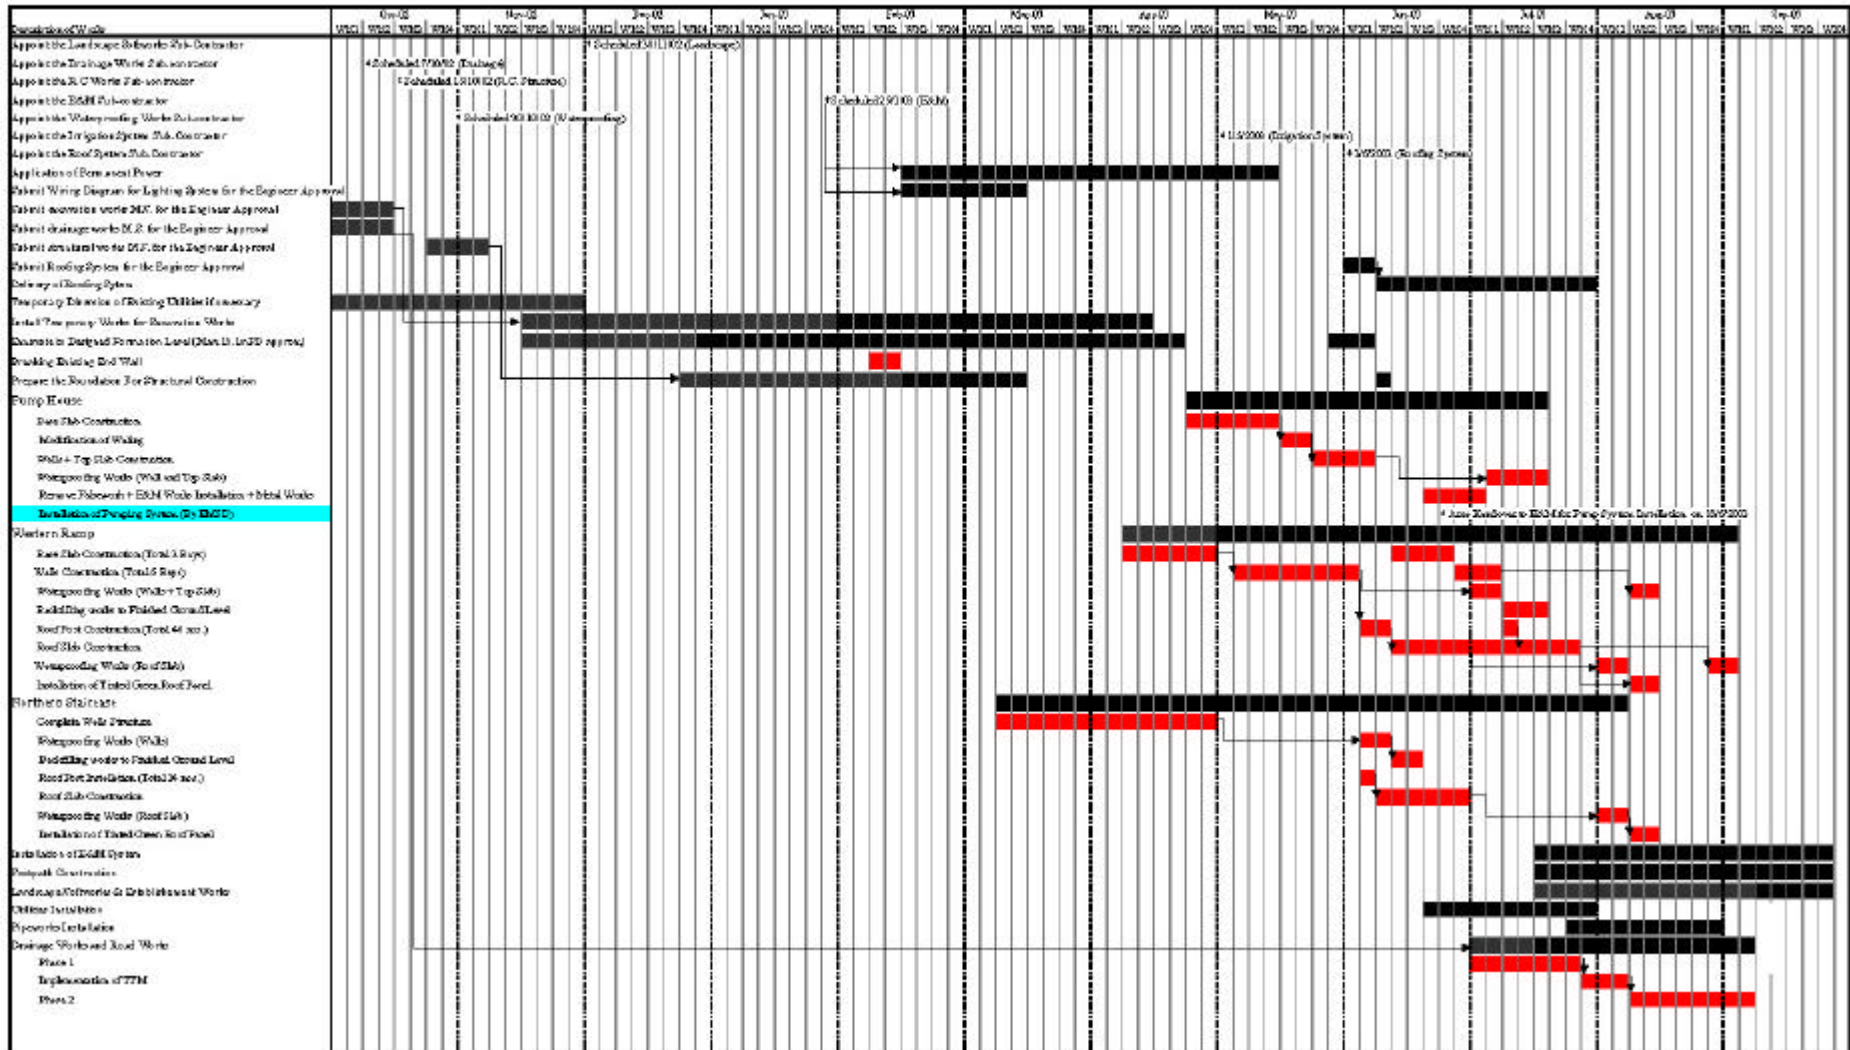

Barbican Construction Limited
 Contract No. BC2001/10
 268 Shek Road (between Shek Kwai Road and Pak Hei Road) TD Project
 Total 26 Working Items for Completion of Works

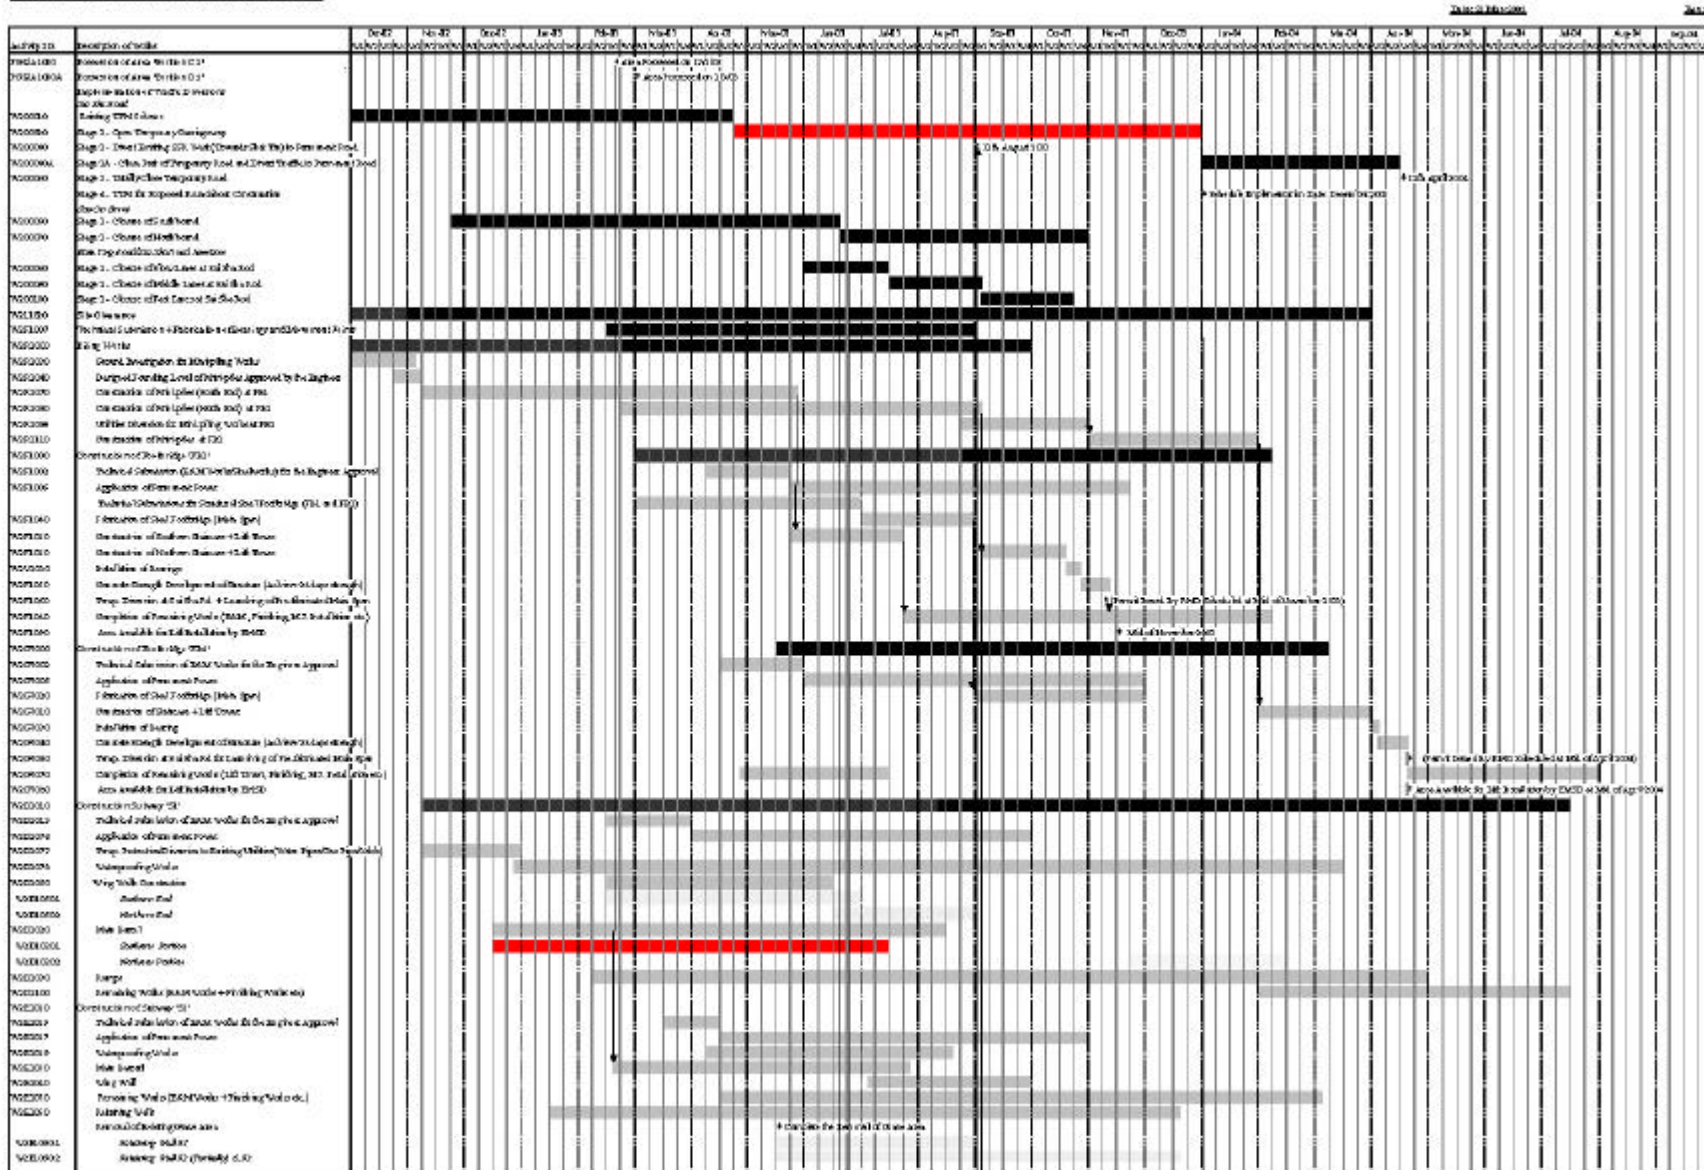

Barbican Construction Limited
 Contract No. H2600/20
 Site 28a Road Widening Between Kam Yag Road and Futara/Tham Road T/J Junction
 Detailed Workline Program under Consideration of Section 2 Works

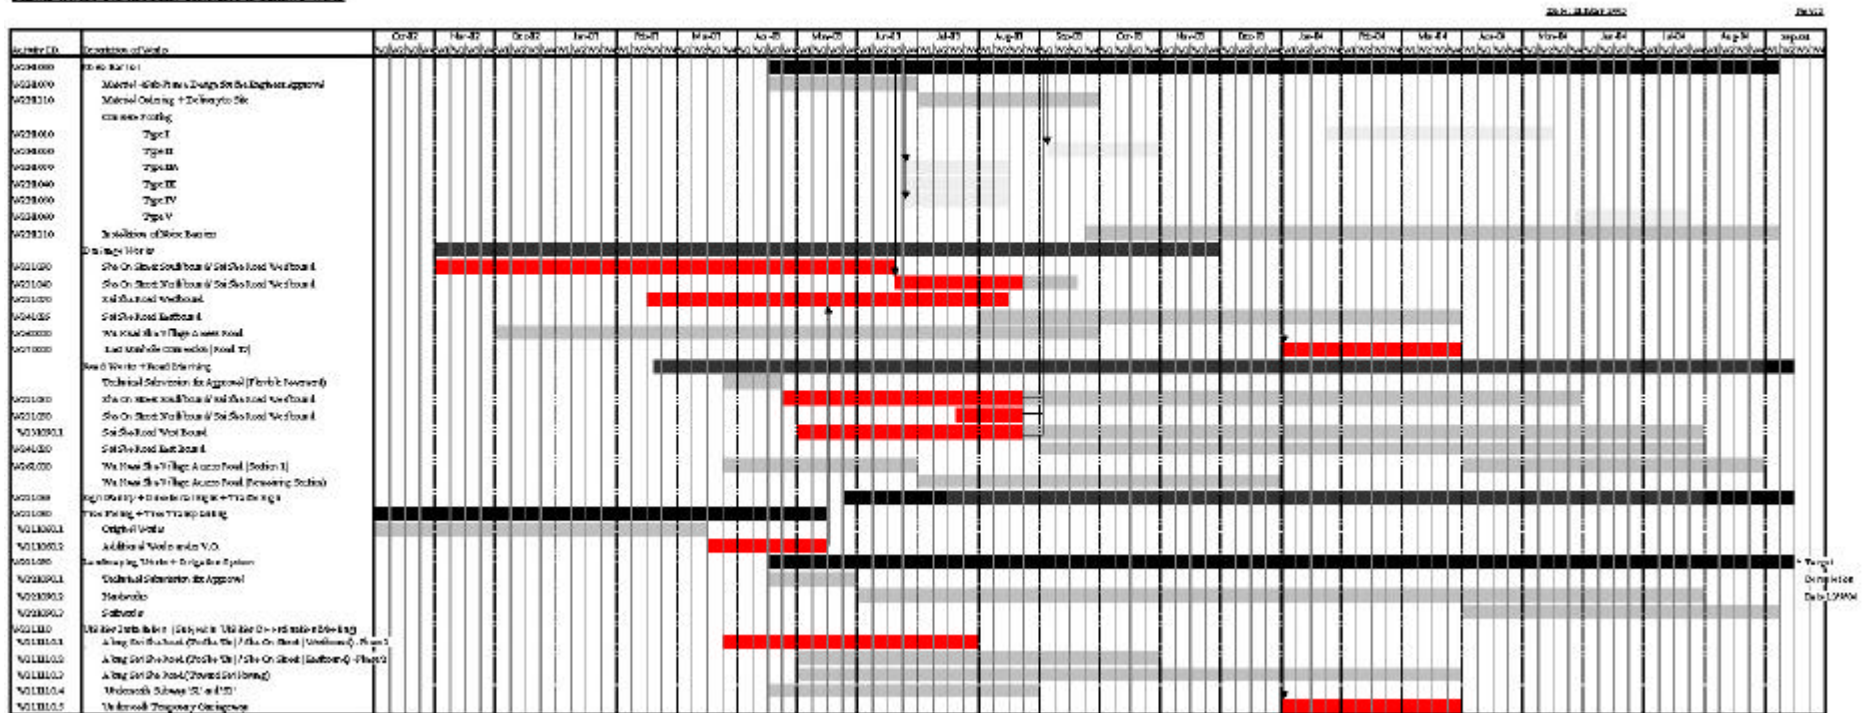




APPENDIX B
SITE ORGANIZATION CHART

Barbican Construction Co., Ltd.

Contract No. : HY/2001/18
 Sai Sha Road Widening between
 Kam Ying Road and Future Trunk Road T7 Junction

Date : 23 September 2002
 Rev : C

Site Organization Chart

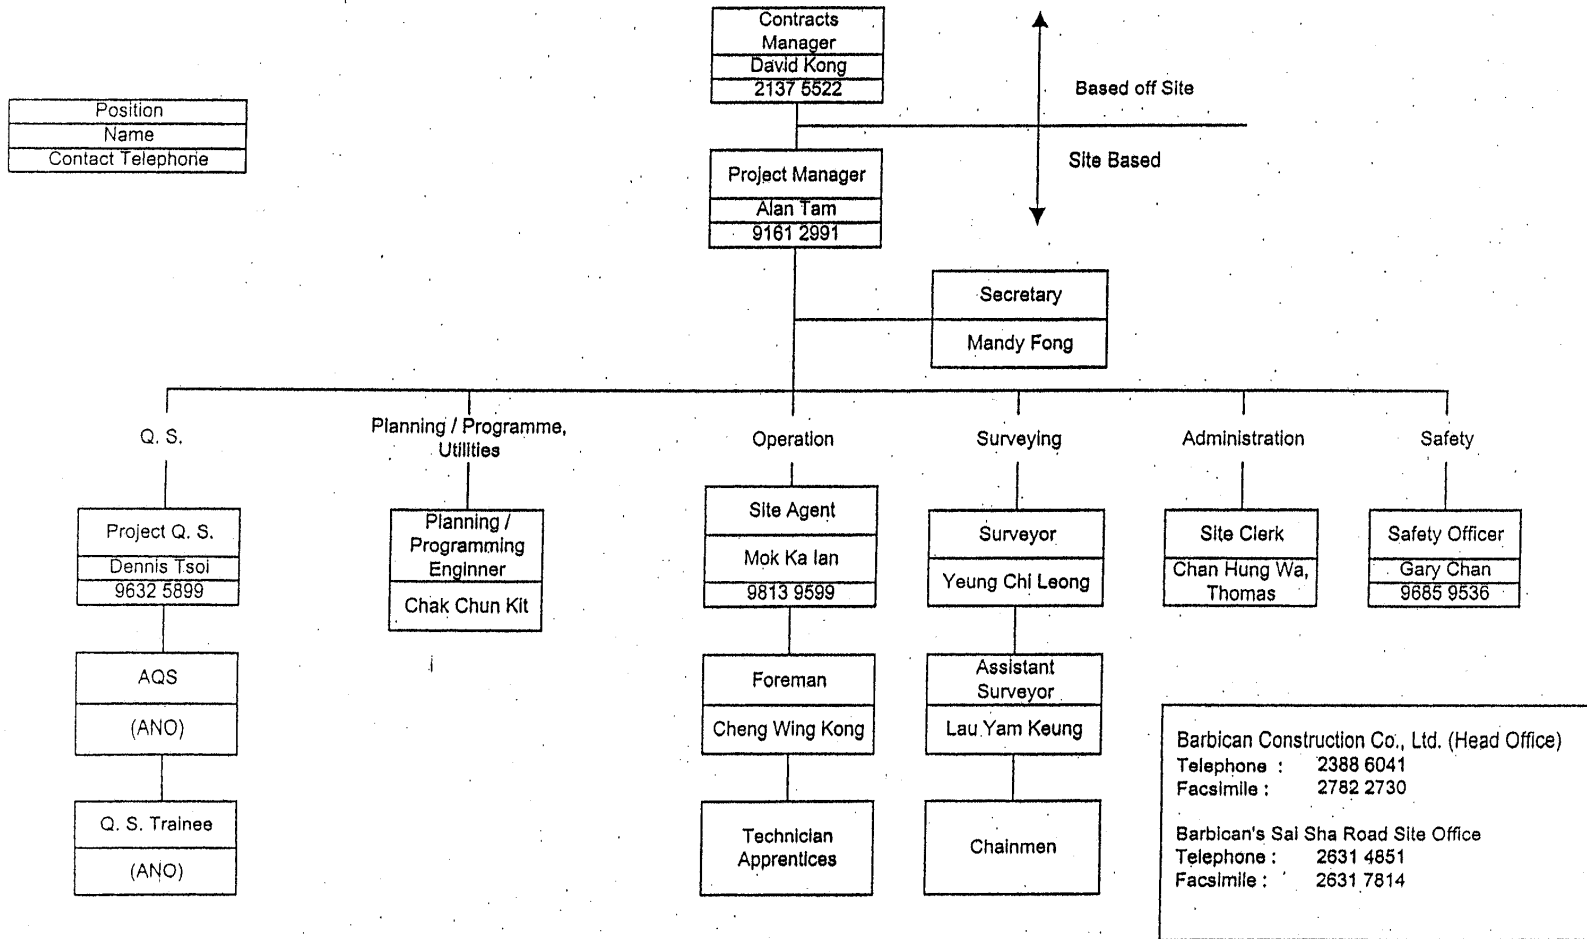



APPENDIX C
RECORD PHOTOS FOR CONSTRUCTION ACTIVITIES
IN JULY 2003



Date: 3 July 2003 Works: Minipile Works for Footbridge
Location: Wu Kwai Sha New Village Access Road



Date: 10 July 2003 Works: Minipile Works for Footbridge
Location: Wu Kwai Sha New Village Access Road



Date: 3 July 2003 Works: Construction of Subway
Location: Near Residential Development Wu Kai Sha DD 206



Date: 10 July 2003 Works: Construction of Subway
Location: Near Residential Development Wu Kai Sha DD 206



Date: 10 July 2003
Location: Near Villa Athena

Works: Construction of Subway




Date: 3 July 2003
Location: Near Villa Athena

Works: Construction of Subway



APPENDIX D
THE PROJECT AREA, ENVIRONMENTAL SENSITIVE RECEIVERS
AND THE LOCATIONS OF THE MONITORING STATIONS

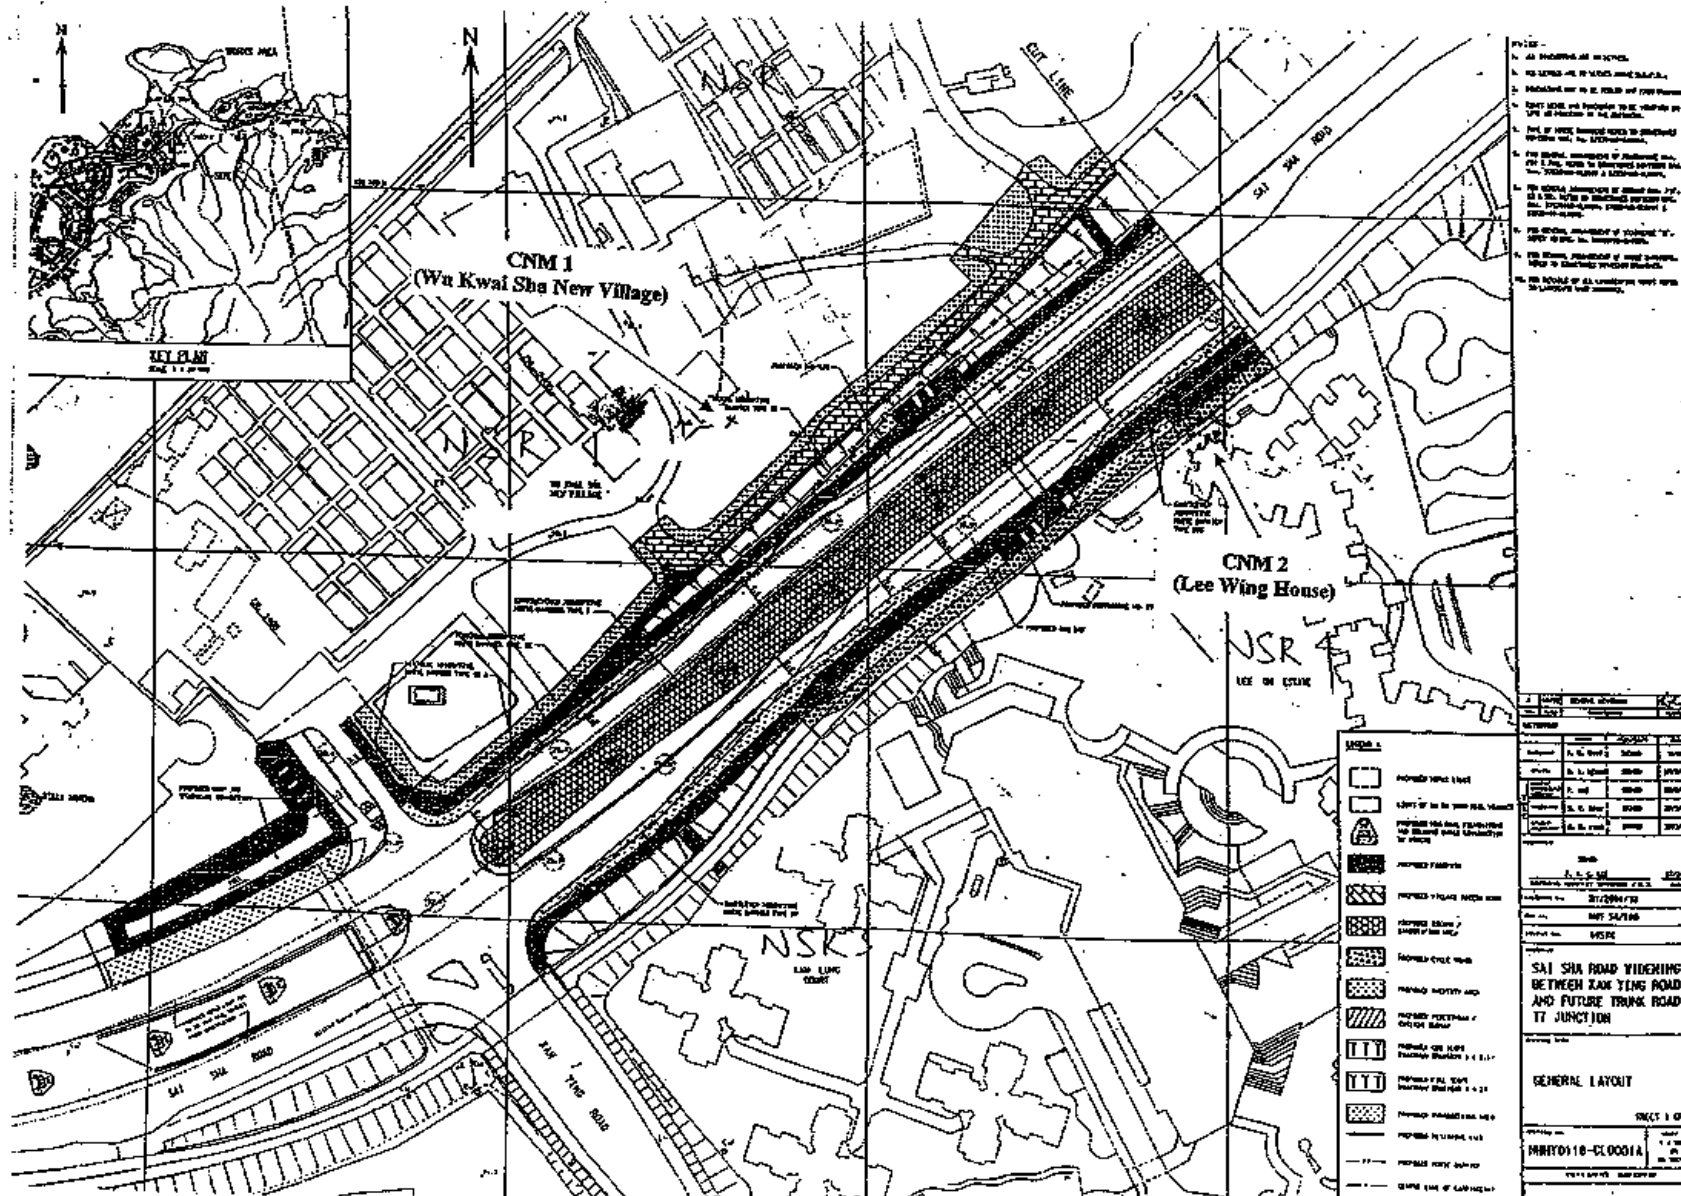



Monitoring Point CNM 1 – Wu Kwai Sha New Village



Monitoring Point CNM 2 – Lee Wing House of Lee On Estate



Monitoring Point CNM 3 – Residential Development at Wu Kai Shs DD 206



APPENDIX E
CALIBRATION CERTIFICATES FOR SOUND LEVEL METER

DICESVA S.L.
Calibration laboratory

CERTIFICATE OF CALIBRATION

NUMBER: 0086E/01

DICESVA S.L.
Calibration laboratory


Villar, 20
08041 BARCELONA
SPAIN
Phone number 934 335 240 / Fax 933 479 310

The calibration has been performed following calibration procedure P015 (Revision 0) for acoustic tests and P016 (Revision 0) for electrical tests, based on standards IEC60651:1979/A1:1993 and IEC60804:1985/A1:1989/A2:1993.

INSTRUMENT:	INTEGRATING-AVERAGING SOUND LEVEL METER
MANUFACTURER:	CESVA
MODEL:	SC-20e
SERIAL NUMBER:	T214258
MICROPHONE:	C130, serial number 5609
TYPE:	1
DATE OF CALIBRATION	acoustical tests: 2001-09-03 electrical tests: 2001-09-04
CALIBRATION RESULT:	Within the specifications in the values measured

Laboratory manager

Date of issue: 2001-11-12



Xavier Solà Gimeno

DICESVA S.L.
Calibration laboratory

CERTIFICATE OF CALIBRATION

NUMBER: 0087E/01

DICESVA S.L.
Calibration laboratory


Villar, 20
08041 BARCELONA
SPAIN
Phone number 934 335 240 / Fax 933 479 310

The calibration has been performed following calibration procedure P017 (Revision 0), based on standard IEC942:1988.

INSTRUMENT:	SOUND CALIBRATOR
MANUFACTURER:	CESVA
MODEL:	CB-5
SERIAL NUMBER:	031198
TYPE:	1L
DATE OF CALIBRATION	2001-10-17
CALIBRATION RESULT:	Within the specifications in the values measured

Laboratory manager

Date of issue: 2001-11-12



Xavier Solà Gimeno



APPENDIX F
DATA OF NOISE MONITORING

Contract No. HY/2001/18

Sai Sha Road Widening between Kam Ying Road

and Future Trunk Road T7 Junction

Monitoring Location: Wu Kwai Sha New Village (CNM 1)

Time Period 7:00-19:00

Date	Start Time	Duration (min)	Measurement Results								
			L ₉₀ (dB(A))	L ₁₀ (dB(A))	L _{eq} (dB(A)) (5 mins)						L _{eq} (dB(A)) (30 mins)
03/07/03	10:00	30	60.5	66.0	65.2	65.1	67.5	63.8	63.8	61.5	64.5
10/07/03	10:05	30	61.7	66.5	62.8	63.3	64.7	64.6	64.8	66.3	64.4
17/07/03	10:01	30	62.7	68.1	66.8	67.0	66.4	64.8	64.2	65.3	65.8
25/07/03	10:07	30	60.0	66.2	62.4	61.1	61.5	62.7	66.3	65.0	63.2

Contract No. HY/2001/18

Sai Sha Road Widening between Kam Ying Road

and Future Trunk Road T7 Junction

Monitoring Location: Kam Lung Court (CNM 2)

Time Period 7:00-19:00

Date	Start Time	Duration (min)	Measurement Results								
			L ₉₀ (dB(A))	L ₁₀ (dB(A))	L _{eq} (dB(A)) (5 mins)						L _{eq} (dB(A)) (30 mins)
03/07/03	10:34	30	62.8	73.3	72.9	67.5	66.1	66.0	70.0	70.9	68.9
10/07/03	10:41	30	63.4	69.9	67.0	67.6	66.5	67.2	67.5	68.0	67.3
17/07/03	10:37	30	63.6	68.5	66.8	66.5	66.8	65.7	66.9	65.8	66.4
25/07/03	10:44	30	62.0	68.3	64.8	65.4	67.2	67.3	65.4	65.9	66.0

Contract No. HY/2001/18

Sai Sha Road Widening between Kam Ying Road

and Future Trunk Road T7 Junction

Monitoring Location: Residential Development at Wu Kai Sha DD206 (CNM 3)


Time Period 7:00-19:00


Date	Start Time	Duration (min)	Measurement Results								Adjustment *	
			L ₉₀ (dB(A))	L ₁₀ (dB(A))	L _{eq} (dB(A)) (5 mins)					L _{eq} (dB(A)) (30 mins)		
03/07/03	11:10	30	61.8	68.9	66.3	66.1	65.5	66.3	68.8	65.8	66.5	69.5
10/07/03	11:17	30	62.1	68.7	66.2	67.2	66.1	66.3	67.8	64.4	66.3	69.3
17/07/03	11:13	30	60.8	68.8	66.5	65.1	66.0	66.3	66.1	64.9	65.8	68.8
25/07/03	11:19	30	60.7	69.3	65.9	66.2	66.7	66.7	67.0	64.2	66.1	69.1


* Note: A correction of + 3dB (A) is made to the free field measurements



APPENDIX G
GRAPHICAL REPRESENTATION OF
CONSTRUCTION NOISE MONITORING DATA

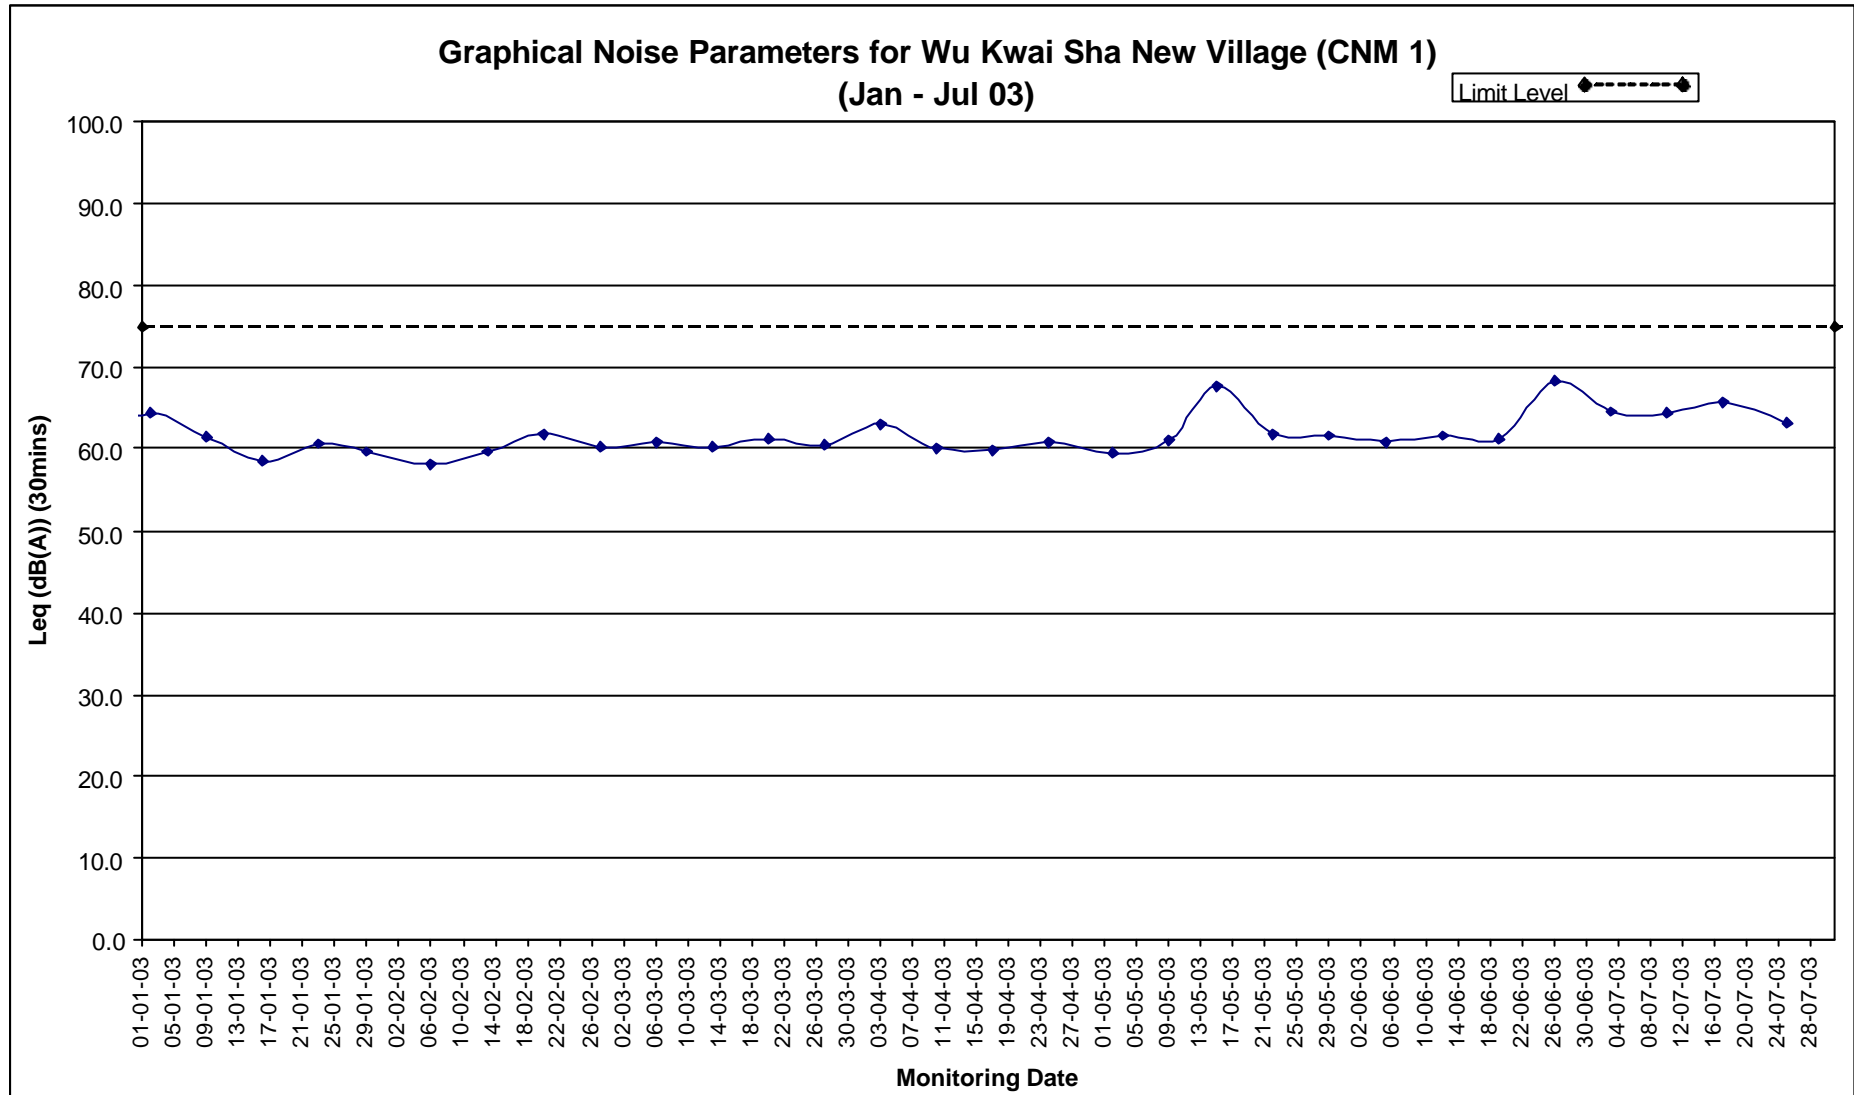

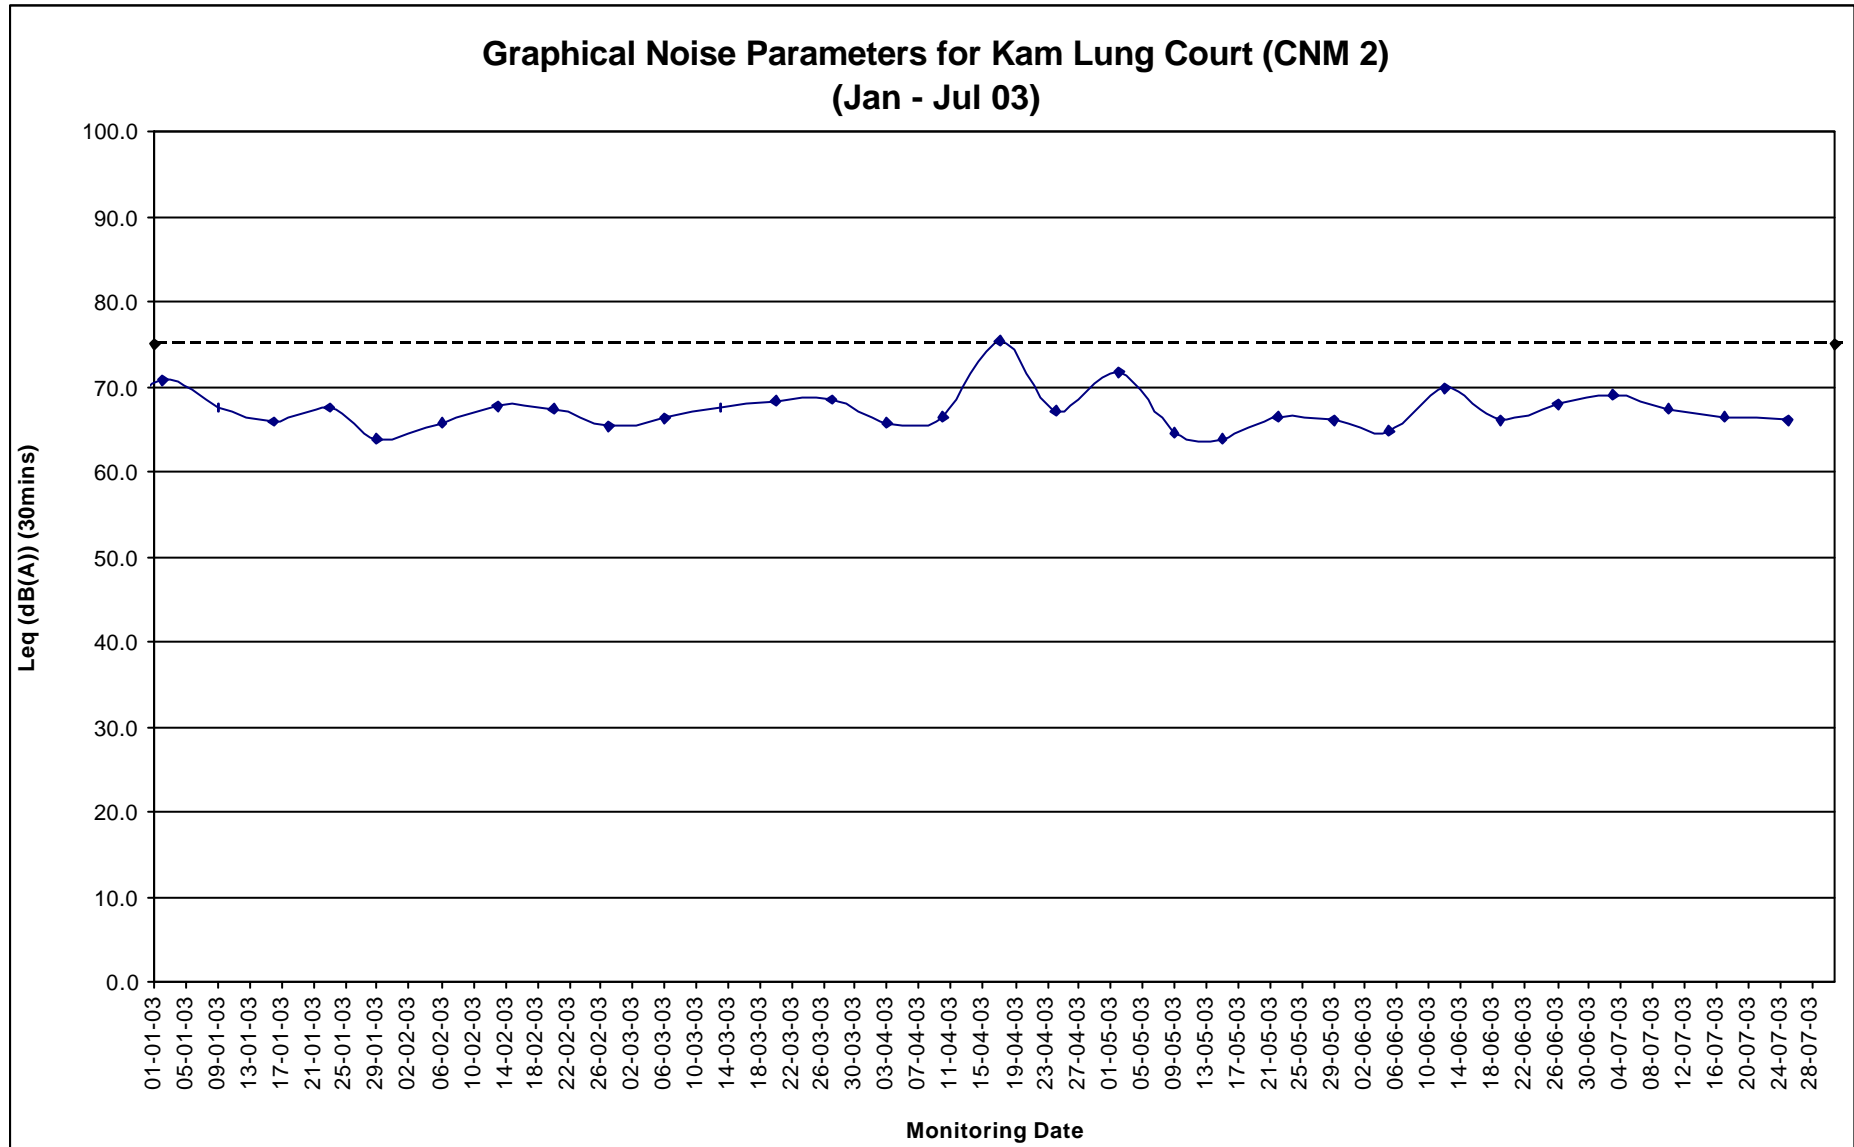

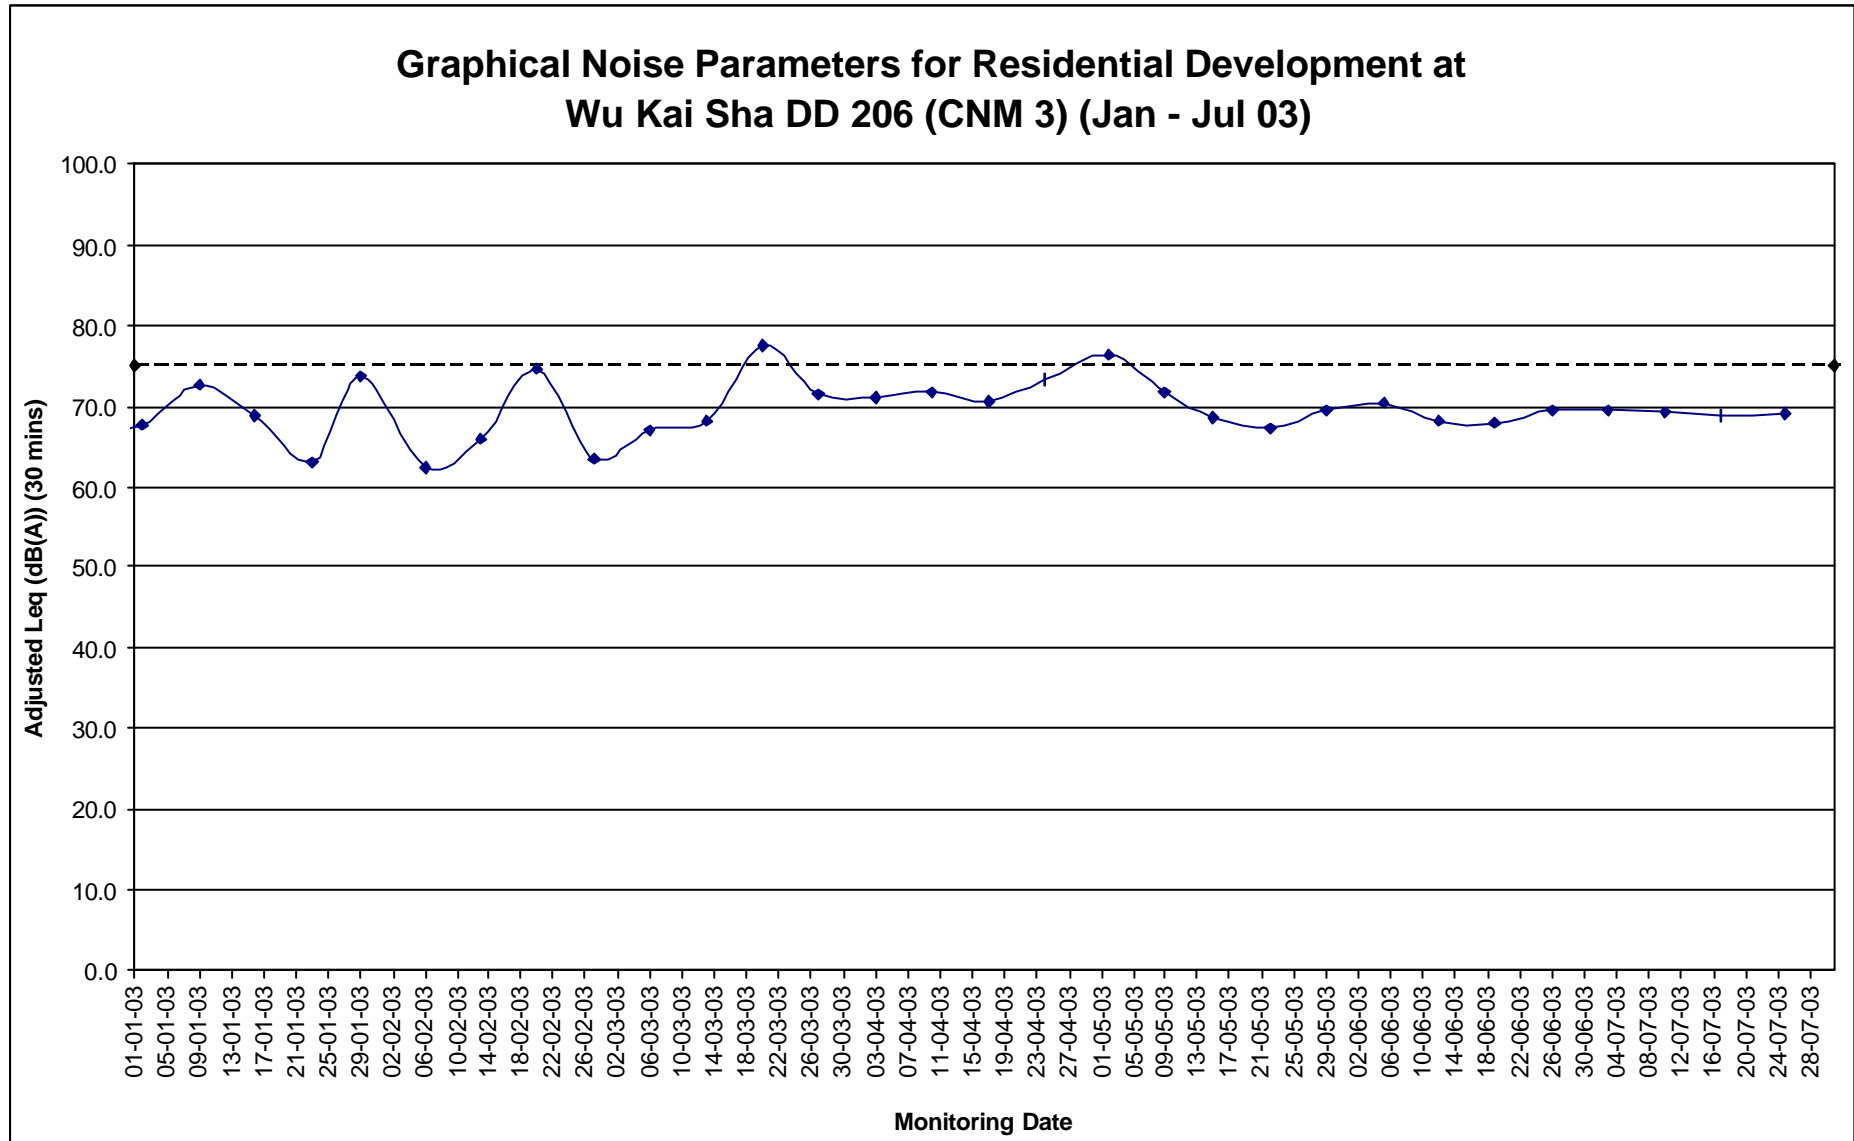



APPENDIX H
WEATHER CONDITIONS
DURING THE MONITORING PERIOD

Contract No.

HY/2001/18

**Sai Sha Road Widening between Kam Ying Road
and Future Trunk Road T7 Junction****Major Activity and Weather Condition During Baseline Monitoring****Monitoring Location: Wu Kwai Sha New Village (CNM 1)**

Date	Start Time	Weather Condition	Major Activities	Other Activities
03/07/03	10:00	Sunny	Backhoe	Traffic
10/07/03	10:05	Sunny	Backhoe	Traffic
17/07/03	10:01	Sunny	Backhoe	Traffic
25/07/03	10:07	Drizzle	Backhoe	Traffic

Contract No.

HY/2001/18

**Sai Sha Road Widening between Kam Ying Road
and Future Trunk Road T7 Junction****Major Activity and Weather Condition During Baseline Monitoring****Monitoring Location: Kam Lung Court (CNM 2)**

Date	Start Time	Weather Condition	Major Activities	Other Activities
03/07/03	10:34	Sunny	Backhoe	Traffic , Pedestrian
10/07/03	10:41	Sunny	Backhoe	Traffic
17/07/03	10:37	Sunny	Backhoe	Traffic , Pedestrian
25/07/03	10:44	Drizzle	Backhoe	Traffic , Pedestrian

Contract No. HY/2001/18

**Sai Sha Road Widening between Kam Ying Road
and Future Trunk Road T7 Junction**

Major Activity and Weather Condition During Baseline Monitoring

Monitoring Location: Residential Development at Wu Kai Sha DD206 (CNM 3)

Date	Start Time	Weather Condition	Major Activities	Other Activities
03/07/03	11:10	Sunny	Backhoe	Traffic
10/07/03	11:17	Sunny	Backhoe	Traffic
17/07/03	11:13	Sunny	Backhoe	Traffic , Pedestrian
25/07/03	11:19	Drizzle	Nil	Traffic



APPENDIX I
CONSTRUCTION NOISE MONITORING LIMIT ACTION LEVEL


According to Section 2.7 of the *EM & A Manual*, the Action and Limit Noise Levels are summarised in the following table:


Time Period	Action	Limit Level
0700-1900 hours on normal weekdays	When one documented complaint is received	75 dB(A)
0700-2300 hours on holidays; and 1900-2300 hours on all other days		70 dB(A)
2300-0700 hours of next day		55 dB(A)


Note: The noise limit level for all the NSRs within this contract is 75dB(A).



APPENDIX J
GRAPHICAL PLOTS OF TRENDS OF MONITORED PARAMETERS

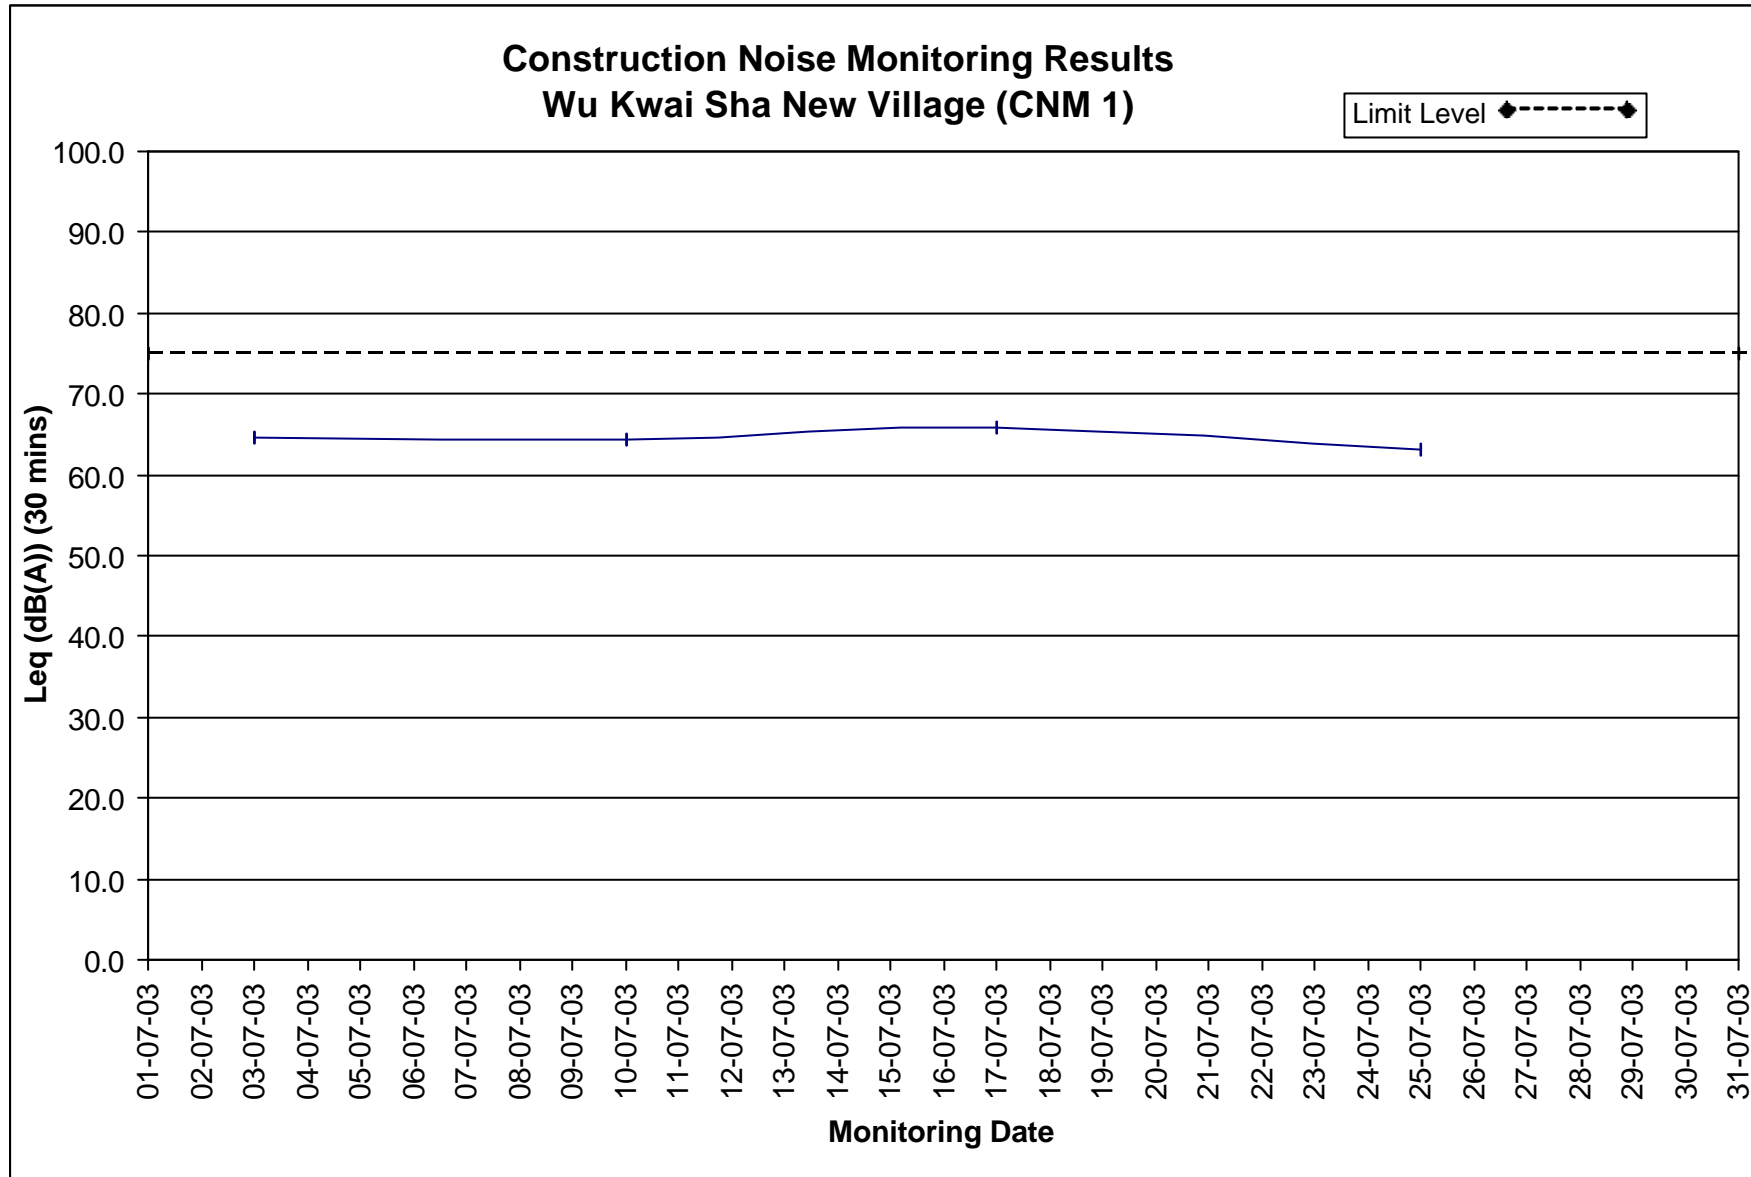

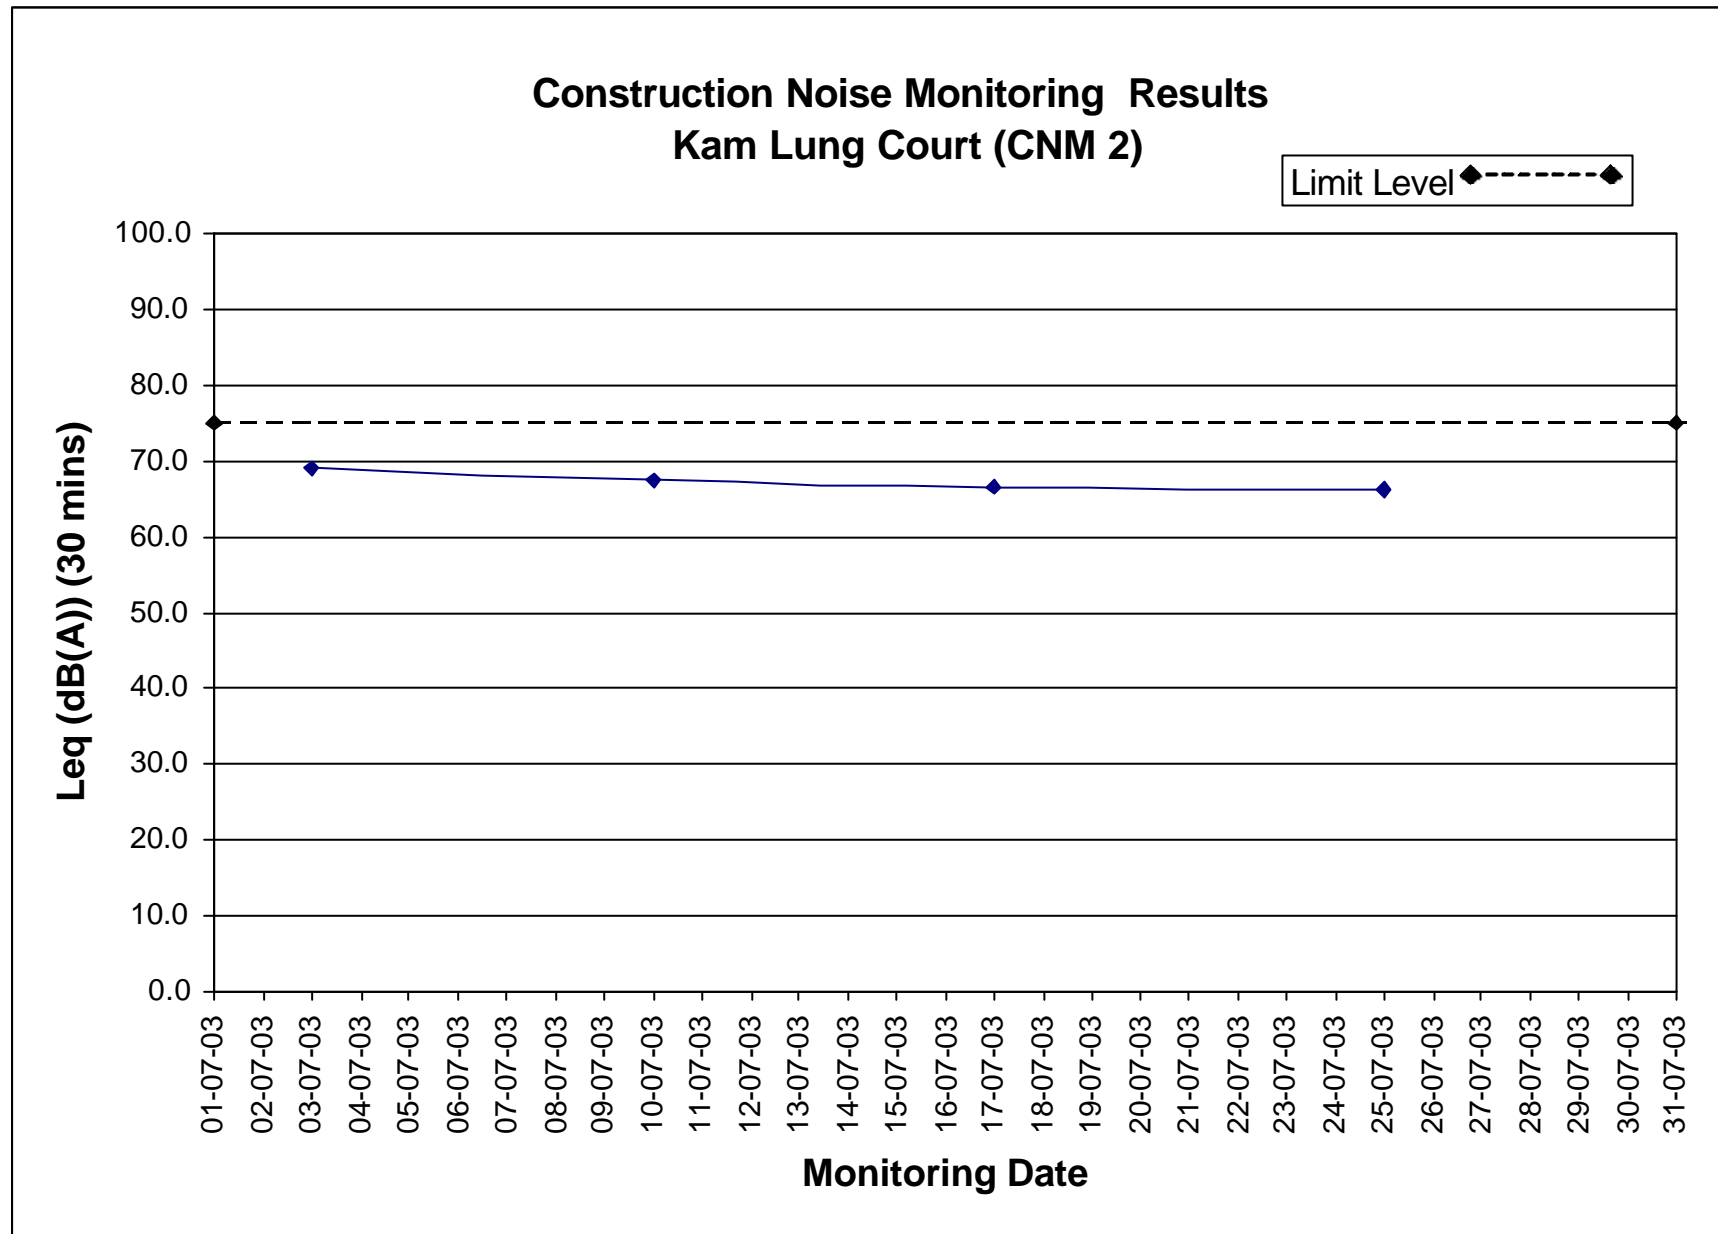

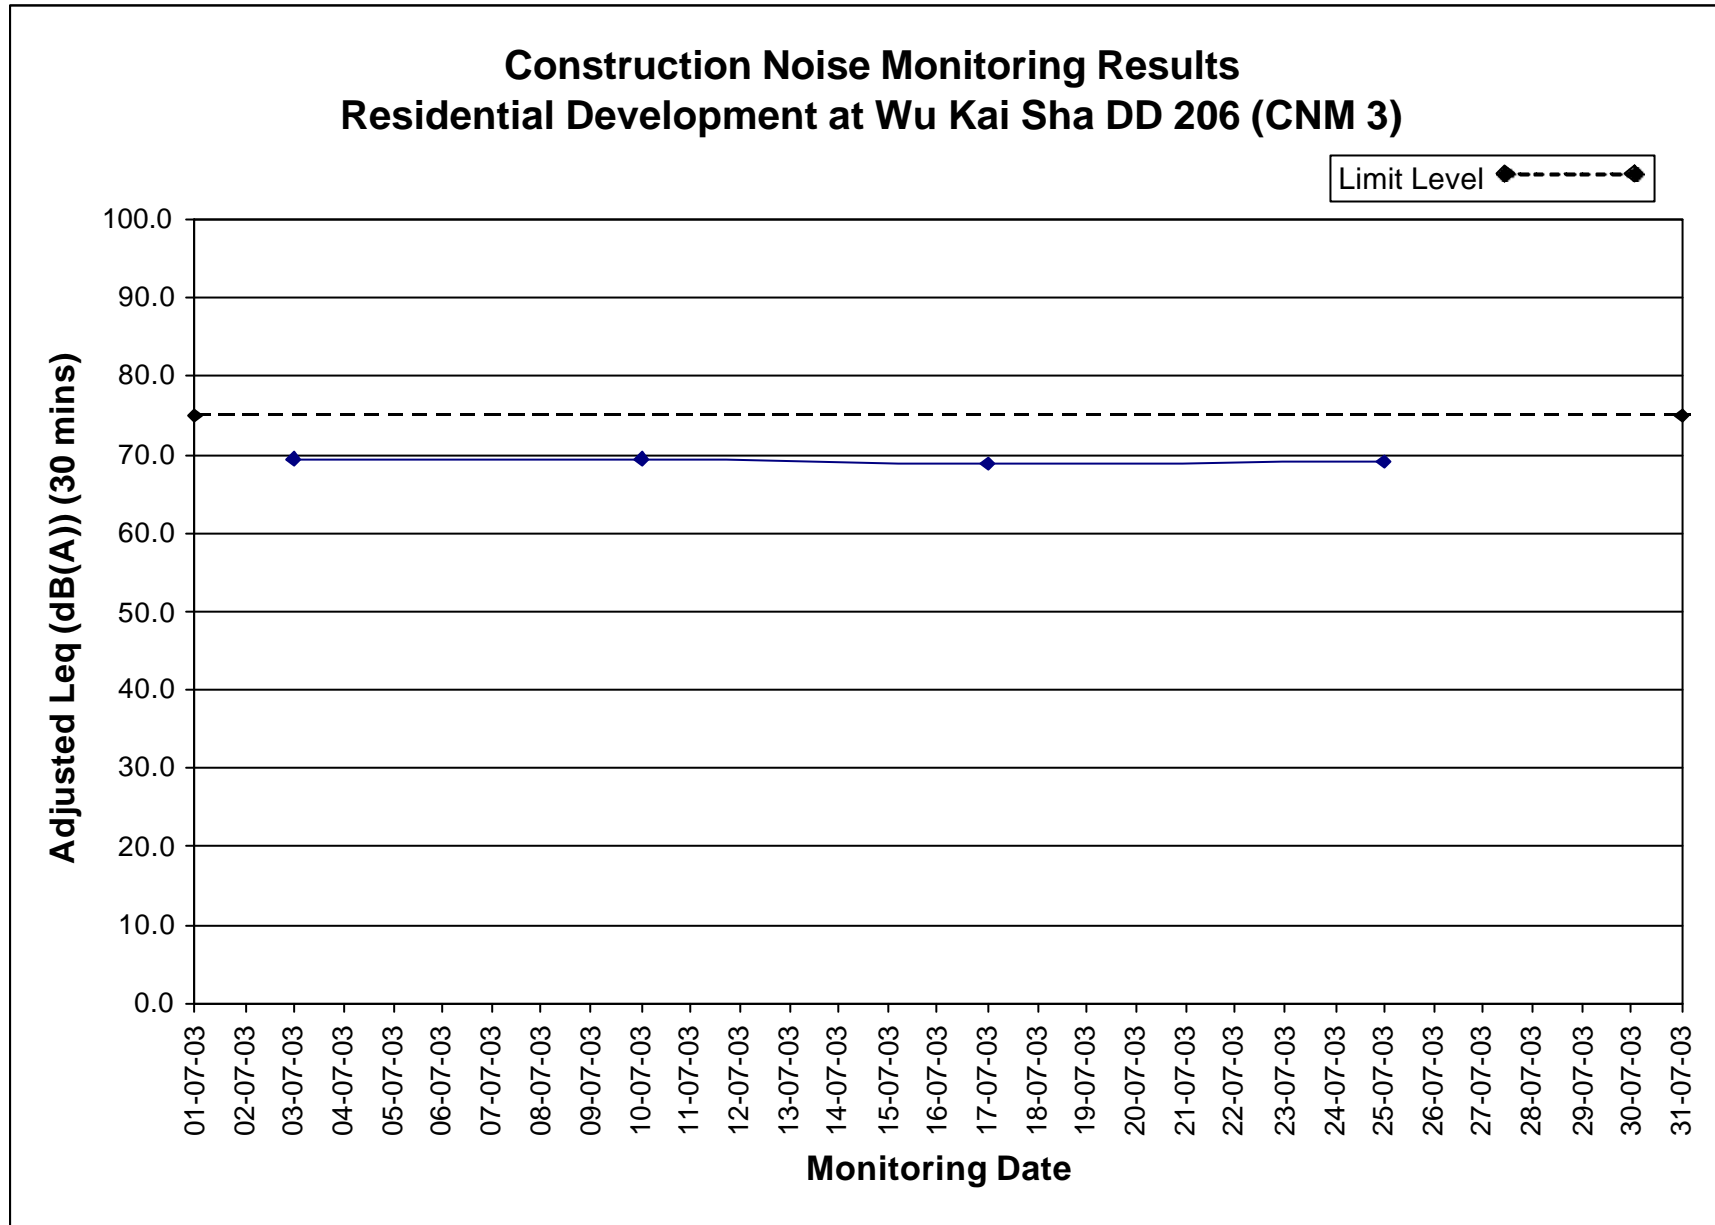



APPENDIX K
CONSTRUCTION NOISE MONITORING SCHEDULES
JULY 2003 AND AUGUST 2003

Job No. : G/2563.01

Contract No. HY/2001/18

Sai Sha Road Widening between Kam Ying Road and Future Trunk Road T7 Junction

Construction Noise Monitoring Schedule**July - August 2003**

Location Point	Monitoring Parameter	Measurement Start Time				
		03/07/2003 (Thursday)	10/07/2003 (Thursday)	17/07/2003 (Thursday)	25/07/2003 (Friday)	01/08/2003 (Friday)
CNM 1	L _{eq} (30 min)	10:00	10:05	10:01	10:07	10:00
CNM 2	L _{eq} (30 min)	10:34	10:41	10:37	10:44	10:40
CNM 3	L _{eq} (30 min)	11:10	11:17	11:13	11:19	--

Location Point	Monitoring Parameter	Measurement Start Time				
		07/08/2003 (Thursday)	14/08/2003 (Thursday)	21/08/2003 (Thursday)	28/08/2003 (Thursday)	
CNM 1	L _{eq} (30 min)	10:00	10:00	10:00	10:00	
CNM 2	L _{eq} (30 min)	10:40	10:40	10:40	10:40	

* Note: In case of poor weather condition on the monitoring date, we will inform the Contractor to arrange another construction noise impact monitoring in a day in the same week.



APPENDIX L
STATISTICS FOR ENVIRONMENTAL COMPLAINTS

**Contract No. HY/2001/18
Sai Sha Road Widening between Kam Ying Road
and Future Trunk Road T7 Junction**

**Statistic for Environmental Complaint
July 2003**

