

**JOB NO.: TCS/00280/05**

**REVISION NO.: 0**

**DRAINAGE SERVICES DEPARTMENT (DSD)  
CONTRACT NO. DC/2004/08**



**PENG CHAU SEWAGE TREATMENT WORKS  
UPGRADE**

**MONTHLY ENVIRONMENTAL MONITORING AND  
AUDIT (EM&A) REPORT FOR JANUARY 2008**

**PREPARED FOR**

**Acciona-ATAL Joint Venture (AAJV)**

**Quality Index**

<b>Date</b>	<b>Reference No.</b>	<b>Prepared by</b>	<b>Certified By</b>
01 February 2008	TCS00280/05/600/R0316	Ben Tam (Project Supervisor)	Ken Wong (Project Environmental Team Leader)
			

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.

## TABLE OF CONTENTS

<b>1.0</b>	<b>INTRODUCTION</b>	<b>1</b>
<b>2.0</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>	<b>2</b>
<b>3.0</b>	<b>SUMMARY OF IMPACT MONITORING REQUIREMENTS</b>	<b>3</b>
<b>4.0</b>	<b>IMPACT MONITORING METHDOLOGY</b>	<b>4</b>
<b>5.0</b>	<b>IMPACT MONITORING RESULTS</b>	<b>8</b>
<b>6.0</b>	<b>WASTE MANAGEMENT</b>	<b>9</b>
<b>7.0</b>	<b>SITE INSPECTION</b>	<b>9</b>
<b>8.0</b>	<b>ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>10</b>
<b>9.0</b>	<b>IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>10</b>
<b>10.0</b>	<b>IMPACT FORECAST</b>	<b>11</b>
<b>11.0</b>	<b>CONCLUSION</b>	<b>11</b>

### List of Tables

Table 2-1	Major Construction Activities in the Reporting Month
Table 2-2	Status of Environmental Licenses and Permits
Table 3-1	Summary of EM&A Requirements
Table 3-2	Action and Limit Levels for Air Quality
Table 3-3	Action and Limit Levels for Construction Noise
Table 3-4	Action and Limit Levels for Marine Water Quality
Table 4-1	Location of Air Quality and Noise Monitoring Station
Table 4-2	Locations of Marine Water Quality Monitoring
Table 4-3	Monitoring Equipment Used in EM&A Program
Table 4-4	Analytical Methods Applied to Marine Water Quality Samples
Table 5-1	Summary of 24-Hour and 1-Hour TSP Monitoring Results
Table 5-2	Summary of Construction Noise Monitoring Results
Table 6-1	Summary of Waste Quantities for Disposal
Table 6-2	Summary of Quantities of Recycling Materials
Table 8-1	Statistical Summary of Environmental Complaints
Table 11-1	Summary of the Exceedances for Impact Monitoring

### List of Appendices

Appendix A	Project Site Layout
Appendix B	Environmental Organisation Structure
Appendix C	Locations of Designated Monitoring Stations
Appendix D	Equipment Calibration Certificates
Appendix E	Impact Monitoring Schedules
Appendix F	Graphical Plots of Air Quality and Construction Noise Monitoring Results
Appendix G	Meteorological Data in the Reporting Period
Appendix H	Three-Month Rolling Program

### Executive Summary

ES.01 Acciona-ATAL Joint Venture (AAJV) has been awarded the DSD Contract DC/2004/08 (Project) for the Peng Chau Sewage Treatment Works Upgrade in May 2005. The Project requires an Environmental Monitoring & Audit (EM&A) program to be implemented by an Environmental Team (ET) throughout the contract period in compliance with the requirements as stated in the project Environmental Permit (EP-203/2004) and the Project EM&A manual.

ES.02 Action-United Environmental Services and Consulting (AUES) has been commissioned by AAJV to be an independent Environmental Team (ET) to implement the EM&A program in compliance with the EP and the project EM&A Manual.

ES.03 This report presents the monitoring results and audit findings under the EM&A program during the reporting month for **January 2007**.

### EM&A Activities in the Reporting Month

ES.04 A summary of the monitoring activities in this reporting month is listed below:

• 1-Hour TSP Monitoring	18 Events
• 24-Hour TSP Monitoring	6 Events
• Construction Noise Monitoring	6 Events
• Marine Water Quality Monitoring	0 Event
• Site Inspection Audit	4 Times

### Air Quality

ES.05 No exceedances of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

### Construction Noise

ES.06 No Limit Level exceedance in construction noise measurements was recorded and no noise complaint (Action Level) was received in this reporting month.

### Marine Water Quality

ES.07 Since all the marine based construction activities had been completed on 1 August 2006, post marine water quality monitoring was commenced on 2 August 2006 and completed on 1 September 2006 in accordance with Clause 4.32 of the EM&A Manual. All the measurement results at the control/impact stations were within the baseline range. The monitoring results were presented in the previous Monthly EM&A Report (September 2006).

### Summary of Monitoring Exceedances

ES.08 A summary of monitoring exceedances in this reporting month for air quality, construction noise and marine water quality monitoring are presented below:

Env. Quality	Parameters	Compliance %	Investigation & Corrective Actions
Air Quality	1-Hour TSP	100	Not Required for 100% Compliance
	24-Hour TSP	100	Not Required for 100% Compliance
Noise	Leq (30min) Daytime	100	Not Required for 100% Compliance
Marine Water Quality*	-	-	-

Note: \*No marine water quality impact monitoring was required since all marine based construction activities were completed on 01 August 2006.

### Environmental Complaints

ES.09 No environmental complaint was received in this reporting month.

### Environmental Summons

ES.10 No environmental summons was received in this reporting month.

### Future Key Issues

ES.11 The potential environmental impacts for this project generally include air quality, noise, water quality and construction waste. The contractor is to properly implement the required environmental mitigation measures as per the Implementation Schedule in the EM&A manual to ensure no significant adverse environmental impact arises from the construction works. The contractor was reminded to maintain good house-keeping throughout the construction period.

## 1.0 INTRODUCTION

- 1.01 Acciona-ATAL Joint Venture (AAJV) has been awarded the DSD Contract DC/2004/08 (Project) for the upgrading of Peng Chau Sewage Treatment Works in May 2005. The Project requires an Environmental Monitoring & Audit (EM&A) program to be implemented by an Environmental Team (ET) throughout the contract period in compliance with the requirements as stated in the project Environmental Permit (EP-203/2004) and the project EM&A manual. The location of the project site is presented in **Appendix A**.
- 1.02 The works to be executed under this project mainly comprise the following:
- Upgrade and reconstruct the existing Peng Chau Sewage Treatment Works (STW);
  - Construct an emergency overflow, storm tanks and submarine outfall;
  - Provide de-odourization facilities and associated sludge treatment facilities, and extend inlet pumping mains and construct an equalization tank;
  - Demolish the existing treatment facilities;
  - Construct sludge drying bed; and
  - Construct remaining works.
- 1.03 Action-United Environmental Services and Consulting (AUES) has been commissioned by AAJV to be the independent environmental team (ET) for implementation of the EM&A program in accordance with the requirements as set out in the EP and the project EM&A manual.
- 1.04 This report presents the monitoring results and audit findings under the EM&A program during the reporting month for **January 2008**.

### REPORT STRUCTURE

- 1.05 The Monthly EM&A report is structured into the following sections:

- Section 1 INTRODUCTION**
- Section 2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS**
- Section 3 SUMMARY OF IMPACT MONITORING REQUIREMENTS**
- Section 4 IMPACT MONITORING METHODOLOGY**
- Section 5 IMPACT MONITORING RESULTS**
- Section 6 WASTE MANAGEMENT**
- Section 7 SITE INSPECTION**
- Section 8 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**
- Section 9 IMPLEMENTATION STATUS OF MITIGATION MEASURES**
- Section 10 IMPACT FORECAST**
- Section 11 CONCLUSIONS**

## 2.0 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

### PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

- 2.01 The organization chart and lines of communication with respect to the on-site environmental management and monitoring program are shown in **Appendix B**.

### CONSTRUCTION PROGRESS

- 2.02 A summary of the major construction activities undertaken in this reporting month is shown in **Table 2-1**.

**Table 2-1 Major Construction Activities in the Reporting Month**

Locations	Description of Construction Activities
Portion P	• Carriageway reinstatement.
Portion Q	-
Portion R	• External wall painting at NTSC; • External wall tiling at ESC; and • Demolishing the existing STC.
Portion S	• Demolishing the temporary pump pit.
Area A	-
Area B	-
Area C	-

### SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.03 A summary of the relevant permits, licences, and/or notifications on environmental protection for the Project during this reporting month is presented in **Table 2-2**.

**Table 2-2 Status of Environmental Licenses and Permits**

Item	Item Description	License/Permit Status
1	Environmental Permit No. : EP-203/2004	Issued at 30 November 2004
2	Air Pollution Control (Construction Dust)	Notified EPD on 17 June 2005
3	Water Pollution Control (Discharge Licence) EP890/W2/XE005	Valid to 30 September 2010
4	Chemical Waste Producer Registration WPN:5213-976-N2449-01	Registration on 03 June 2005
5	Marine Dumping Permit (No. EP/MD/06-021)	Expired
6	Exemption for site concrete batching plant licence	Issued at 21 October 2005
7	Exemption Account for Disposal of Construction Waste ( Account Number : 5000577)	Valid until 27 September 2008

### 3.0 SUMMARY OF IMPACT MONITORING REQUIREMENTS

- 3.01 Environmental monitoring and audit requirements are set out in the project EM&A manual. Air quality, construction noise and marine water quality have been identified as the key environmental issues under this project during the construction phase.
- 3.02 A summary of the EM&A requirements for air quality, construction noise and marine water quality monitoring are shown in **Table 3-1**. The designated station/locations for air quality, construction noise and marine water quality monitoring are shown in **Appendix C**.

**Table 3-1 Summary of EM&A Requirements**

Environmental Aspect	Monitoring Parameters	
Air Quality	1-Hour TSP	
	24-Hour TSP	
Construction Noise	Leq <sub>(30min)</sub> during normal working hours	
	Supplementary L <sub>10</sub> and L <sub>90</sub> for reference.	
Marine Water Quality	<ul style="list-style-type: none"> <li>• Dissolved Oxygen (DO);</li> <li>• Temperature;</li> <li>• Turbidity;</li> <li>• pH;</li> </ul>	<ul style="list-style-type: none"> <li>• Salinity;</li> <li>• Suspended Solids (SS);</li> <li>• Ammonia Nitrogen; and</li> <li>• Total Inorganic Nitrogen.</li> </ul>

- 3.03 Air quality monitoring is carried out once in every six days for 24-Hour TSP and 3 times every six days for 1-Hour TSP at the designated monitoring station.
- 3.04 Construction noise monitoring is conducted once in every six days at the designated monitoring station. Measurements of Leq<sub>(30min)</sub> shall be taken between 0700 and 1900 with supplementary L<sub>10</sub> and L<sub>90</sub> data will be collected.
- 3.05 Marine water quality monitoring is carried out 3 times every week at 4 designated monitoring locations (2 Control stations and 2 Impact stations).
- 3.06 The impact marine water quality monitoring program shall be conducted during the course of marine based construction activities of the Project.
- 3.07 A summary of the Action/Limit (A/L) Levels for air quality, construction noise and marine water quality are shown in **Tables 3-2, 3-3 and 3-4**.

**Table 3-2 Action and Limit Levels for Air Quality**

Monitoring Location	Action Level (µg/m <sup>3</sup> )		Limit Level (µg/m <sup>3</sup> )	
	1-Hour TSP	24-Hour TSP	1-Hour TSP	24-Hour TSP
AN1	> or = 346	> or = 163	> or = 500	> or = 260

**Table 3-3 Action and Limit Levels for Construction Noise**

Monitoring Period	Action Level in dB(A)	Limit Level in dB(A)
0700-1900 hours on normal weekdays	When one or more documented complaint was received	> 75 dB(A)

**Table 3-4 Action and Limit Levels for Marine Water Quality**

Parameters		Action Level	Limit Level
DO mg/L	Surface & Mid-depth	< or = 4.1	< or = 3.9
	Bottom	< or = 3.3	< or = 2.0
Turbidity, NTU		6.2 or 120% of upstream control station's SS at the same tide of the same day.	7.5 or 130% of upstream control station's SS at the same tide of the same day.
SS, mg/L		17.6 or 120% of upstream control station's SS at the same tide of the same day.	20.2 or 130% of upstream control station's SS at the same tide of the same day.
NH3-N, mg/L		> or = 0.16	> or = 0.22
TIN, mg/L		> or = 0.91	> or = 0.94
E.Coli, cfu/100mL		> or = 374	> or = 610

3.08 The Event Action Plan for air quality, construction noise and marine water quality has been implemented in this project. Details of the Event Action Plan were presented in the First Impact EM&A report.

#### 4.0 IMPACT MONITORING METHDOLOGY

##### MONITORING LOCATIONS

4.01 There is one designated station for air quality and construction noise monitoring and four (4) designated locations for marine water quality monitoring. Their locations are shown in **Tables 4-1** and **4-2** and geographically in **Appendix C**.

4.02 Owing to the residents' refusal of providing access to the designated air quality and construction noise station, an alternative air and noise monitoring station was proposed and approved by EPD (Ref: (2) EP2/N9/F/93 IV) on 14 July 2005. The approved alternative air and noise station is located at the abutment (Portion P) within the site boundary next to the sensitive receiver Sea Crest Villa.

**Table 4-1 Location of Air Quality and Noise Monitoring Station**

Station ID	Description
AN1	Abutment at Portion P next to Sea Crest Villa

**Table 4-2 Locations of Marine Water Quality Monitoring**

Locations ID	Description	Easting	Northing
W1	Predicted Dredging Non-Impact Zone	821279.0	816452.1
W2	Live Coral Area	821573.2	816769.7
C1	Control Station	821919.0	817155.0
C2	Control Station	821443.2	816257.4

4.03 The installation of a wind monitoring station at the sensitive receivers or site offices was confirmed impractical. Use of meteorological data provided by the Peng Chau Station of the Hong Kong Observatory (HKO) has been adopted in this project since September 2005.

#### MONITORING FREQUENCY AND PERIOD

##### 1-HOUR TSP MONITORING

4.04 All 1-Hour TSP monitoring was conducted at the EPD-approved alternative station three times every 6 days. A total of 18 monitoring events were carried out in this reporting period.



**24-HOUR TSP MONITORING**

4.05 All 24-Hour TSP monitoring was conducted at the EPD-approved alternative station once every six days. Power shortage was reported by the Contractor on 25 January 2008. Therefore, only 5 monitoring events were carried out in this reporting period.

**CONSTRUCTION NOISE MONITORING**

4.06 Impact construction noise monitoring was undertaken at the EPD-approved alternative location weekly. A total of 6 monitoring events were carried out in this reporting period.

**MARINE WATER QUALITY MONITORING**

4.07 Since the submarine work was completed on 01 August 2006, therefore no impact water quality monitoring had been undertaken in this reporting period. According to the EM&A Clause 4.32, post water quality monitoring had been conducted from 02 August 2006 to 01 September 2006. All the measurement results at the control/impact stations were within the baseline range. The monitoring results were presented in the pervious Monthly EM&A Report (September 2006).

**MONITORING EQUIPMENT**

4.08 The monitoring equipment used by the ET in the EM&A program is presented in the **Table 4-3**.

**Table 4-3 Monitoring Equipment Used in EM&A Program**

<b>Environmental Aspect</b>	<b>Parameters</b>	<b>Monitoring Equipment</b>
Marine Water Quality	Dissolved Oxygen	YSI 85
	Temperature	YSI 85
	Turbidity	HACH 2100P
Air Quality	1-Hour TSP	Sibata LD-3
	24-Hour TSP	Tisch High Volume Sampler 515N
Construction Noise	Leq30	B&K Type 2238
	On-site Calibration	B&K Type 4231

**24-HOUR TSP MONITORING**

4.09 24-Hour TSP monitoring was carried out by a High Volume Sampler (HVS) in compliance with the project EM&A Manual. The HVS employed complied with the PS specifications including.

- Power supply of 220v/50 Hz for 24-Hour continuous operation;
- 0.6-1.7 m<sup>3</sup>/min (20-60 SCFM) adjustable flow rate;
- A 7-day mechanical timer for 24-Hour operation;
- An elapsed time indicator with ±2 minutes accuracy for 24-Hour operation;
- Minimum exposed area of 63 in<sup>2</sup>;
- Flow control accuracy of ±2.5% deviation over 24-Hour operation;
- An anodized aluminum shelter to protect the filter and sampler;
- A motor speed-voltage control to control mass flow rate with accuracy of ±2.5% deviation over 24-Hour sampling period;
- Provision of a flow recorder for continuous monitoring;
- Provision of a peaked roof inlet;
- Incorporation with a manometer; and
- An 8"x10" stainless steel filter holder to hold, seal and easy to change the filter paper.

- 4.10 The filter papers used in 24-Hour TSP monitoring were of size 8"x10" and provided by a local HOKLAS-accredited laboratory, ALS Techichem Pty (HK) Limited (HOKLAS No. 66). The filters papers after measurements were returned to the laboratory for the required treatment and analysis.

#### **1-HOUR TSP MONITORING**

- 4.11 Measurements of 1-Hour TSP monitoring were taken by a Sibata LD-3 Laser Dust Meter that is a portable and battery-operated laser photometer capable of performing real time 1-Hour TSP measurements. A comparison test with HVS was carried out prior to baseline monitoring in compliance with the EM&A requirements and a conversion factor for direct reading of the dust meter has been established.

#### **WIND DATA MONITORING**

- 4.12 The installation of a wind monitoring station at the sensitive receivers or site offices was confirmed impractical. The meteorological data for this project has been provided by the Hong Kong Observatory (HKO) Peng Chau Station upon IEC & EPD approval.

#### **NOISE MONITORING**

- 4.13 Noise measurements were taken in terms of the A-weighted equivalent sound pressure level (Leq) measured in decibels (dB). Supplementary statistical results such as L<sub>10</sub> and L<sub>90</sub> were also obtained for reference.
- 4.14 Hand-held sound level meters (B&K Model 2238) and associated acoustical calibrators in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specification were used for taking the impact noise measurements.
- 4.15 Windshield was fitted in all measurements. All noise measurements were made with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq).
- 4.16 No noise measurement was carried out in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s.

#### **MARINE WATER QUALITY MONITORING**

- 4.17 The marine water quality monitoring was carried out in compliance with the project EM&A requirements. Monitored parameters include Dissolved Oxygen (DO), Temperature, Turbidity, Salinity, pH, Suspended Solids (SS) and Total Inorganic Nitrogen (TIN).
- 4.18 DO, temperature, turbidity, pH and salinity were measured in-situ whereas SS and TIN were determined in a HOKLAS accredited laboratory.
- 4.19 Marine water quality monitoring was conducted during mid-ebb and mid-flood at specified depths in compliance with the project EM&A Manual. Duplicate in-situ measurements were taken and duplicate samples were collected in accordance with HOKLAS requirements for QA/QC purposes.

#### LABORATORY MEASUREMENT/ANALYSIS

- 4.20 Laboratory analyses of SS, TIN and ammonia nitrogen were carried out by a local HOKLAS- accredited laboratory, ALS Techichem Pty (HK) Limited (HOKLAS No. 066). The specified testing services provided by ALS as shown in **Table 4-4** are accredited under the HOKLAS Scheme.

**Table 4-4 Analytical Methods Applied to Marine Water Quality Samples**

Determinant	Standard Method	Detection Limit
Suspended Solids (mg/L)	ALS Method EA-025	2.0 mg/L
Total Inorganic Nitrogen (mg/L)	ALS Method EK-055A	0.01 mg/L
Ammonia Nitrogen (mg/L)	ALS Method EK-055A	0.01 mg/L

#### EQUIPMENT CALIBRATION

- 4.21 Initial calibration of the HVS was performed upon installation and thereafter at bi-monthly intervals in accordance with the manufacturer's instruction using the NIST-certified standard calibrator. The calibration data are properly documented and the records are maintained by ET for future reference.
- 4.22 The 1-Hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment is checked before and after each monitoring event. A comparison test was carried out with a HVS. A conversion factor (K) of 4.0 was generated in accordance with the equipment manufacturer's instruction. The meter counts in minutes multiplied by the conversion factor will generate the equivalent dust concentration by HVS.
- 4.23 The sound level meters are calibrated using an acoustic calibrator prior to and after measurements. The meters are regularly calibrated in accordance with the manufacturer's instructions. Prior to and following each noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements are considered valid only if the calibration levels before and after the noise measurement agree to within 1.0 dB.
- 4.24 All in-situ water monitoring instruments are checked, calibrated and certified by a HOKLAS accredited laboratory before use and subsequently re-calibrated at 3-monthly intervals. Responses of sensors and electrodes are checked with standard solutions before each use.
- 4.25 The calibration certificates of the monitoring equipment used during the impact monitoring program are attached in **Appendix D**.

#### DATA MANAGEMENT AND DATA QA/QC CONTROL

- 4.26 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house certified (ISO 9001:2000) Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring program.
- 4.27 The monitoring data recorded in the equipment e.g. 1-Hour TSP meters and noise meters are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data.

4.28 For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

## 5.0 IMPACT MONITORING RESULTS

5.01 The impact EM&A program was carried out by the ET in compliance with the project EM&A Manual in this reporting period. The impact monitoring schedules are presented in **Appendix E** and the monitoring results are detailed in the following sub-sections.

### AIR QUALITY

5.02 The impact air quality monitoring data is summarized in **Tables 5-1**. Graphical plots of the 24-Hour TSP and 1-Hour TSP results are shown in **Appendix F** respectively.

**Table 5-1 Summary of 24-Hour and 1-Hour TSP Monitoring Results**

Monitoring Date	24-Hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-Hour TSP Monitoring Results ( $\mu\text{g}/\text{m}^3$ )				
		Monitoring Date	Start Time	1 <sup>st</sup> Result	2 <sup>nd</sup> Result	3 <sup>rd</sup> Result
28-Dec-07	25	28-Dec-07	9:03	124	127	142
03-Jan-08	25	03-Jan-08	8:56	74	87	83
09-Jan-08	22	09-Jan-08	9:03	148	161	162
14-Jan-08	34	14-Jan-08	9:05	71	86	67
19-Jan-08	31	19-Jan-08	9:00	71	68	70
25-Jan-08	No Power	25-Jan-08	9:04	146	152	154
<b>Action Level</b>	<b>&gt; or = 163</b>	-	-	<b>&gt; or = 346</b>		
<b>Limit Level</b>	<b>&gt; or = 260</b>	-	-	<b>&gt; or = 500</b>		

Note: \* Exceedances are in bold and underline.

5.03 No Action/Limit Level exceedance of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

5.04 The meteorological data in this reporting month are summarized in **Appendix G**.

### CONSTRUCTION NOISE

5.05 The impact noise monitoring results are summarized in **Table 5-2**. Graphical plots of the monitoring data are presented in **Appendix F**.

**Table 5-2 Summary of Construction Noise Monitoring Results**

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6 <sup>th</sup> Leq5	Leq30	Corrected* Leq30
28-Dec-07	9:55	59.1	64.9	59.4	57.6	62.2	64.8	62.2	65
03-Jan-08	9:04	60.5	60.1	59.5	64.6	60.6	64.1	62.1	65
09-Jan-08	9:17	58.2	67.2	62.1	65.6	58.4	58.6	63.2	66
14-Jan-08	9:13	62.6	62.9	63.8	66.7	65.0	69.7	65.9	69
19-Jan-08	9:14	58.0	59.4	63.4	55.6	54.6	61.6	59.8	63
25-Jan-08	9:09	65.9	62.4	58.7	61.8	63.2	67.0	64.0	67
<b>Limit Level</b>		-						-	<b>&gt; 75 dB(A)</b>

Note: \* A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

### MARINE WATER QUALITY

5.06 No marine water quality impact monitoring was required in this reporting month since all marine based construction works had been completed on 01 August 2006.

5.07 Based on the Project EM&A Manual Clause 4.32 requirement, the post marine water quality monitoring had been conducted from 02 August 2006 to 01 September 2006. All the measurement results at the control/impact stations were within the baseline range. The monitoring results were presented in the pervious Monthly EM&A Report (September 2006).

## 6.0 WASTE MANAGEMENT

6.01 The waste management carried by ET was performed on 28 January 2008 in this reporting month, no observation was recorded.

### RECORDS OF WASTE QUANTITIES

6.02 All types of waste arising from the construction work are classified into the following:

- Excavated material;
- Construction & demolition (C&D) material;
- Chemical waste; and
- General refuse.

6.03 The quantities of waste for disposal in this reporting month are summarized in **Tables 6-1** and **6-2**. Whenever possible, materials were reused on-site as far as practicable.

**Table 6-1 Summary of Waste Quantities for Disposal**

Type of Waste	Quantity	Disposal Locations
Excavated Material (Spent lube oil) (Liters)	-	N/A
Empty Site Vehicle Batteries (Nos.)	-	N/A
Excavated material (Uncontaminated) (m <sup>3</sup> )	319.20m <sup>3</sup>	Peng Chau Transfer Facility
Broken Rock (m <sup>3</sup> )	4.11m <sup>3</sup>	Peng Chau Transfer Facility
Construction & Demolition Material (Inert) (tons)	838.12tons	Peng Chau Transfer Facility
Construction & Demolition Material (Non-Inert) (tons)	-	N/A
Asbestos C&D Materials (m <sup>3</sup> )	-	N/A
Chemical Waste (Liters)	-	N/A
Wastewater Collected for Off-site Treatment (m <sup>3</sup> )	-	N/A
General Refuse (tons)	-	Peng Chau Transfer Facility
Dredged Materials (m <sup>3</sup> )	-	N/A

**Table 6-2 Summary of Quantities of Recycling Materials**

Type of Waste	Quantity	Disposal Locations
Recycled Metal (kg)	-	NA
Recycled Paper (kg)	-	NA
Recycled Plastic (kg)	-	NA

## 7.0 SITE INSPECTION

7.01 Representatives of the Engineer and the Contractor carried out joint site inspection every week to evaluate the site environmental performance. The monthly IEC site audit was carried out on 28 January 2008. No non-compliance was noted and some observations were made on general site housekeeping and equipments maintenance.

7.02 Details of the observations and recommendations were recorded during the joint site inspection as follows:

- A 200L diesel oil drum oil located near the site entrance was not properly labeled. AAJV should properly label that oil drum;
- The Contractor was reminded to cover dusty stockpiles/materials including soil and sand after used;

- Drip trays were provided for the chemical containers to prevent soil contamination;
- The Contractor was reminded to cover the chemical containers by impervious sheet when not being used; and
- The Contractor was reminded to remove stagnant water after raining.

## 8.0 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

### ENVIRONMENTAL COMPLAINT AND PROSECUTION

8.01 No environmental complaint was received in this reporting month. The statistical summary table of environmental complaint is presented in **Table 8-1**.

8.02 No environmental summons and prosecution was received in this reporting month.

**Table 8-1 Statistical Summary of Environmental Complaints**

Reporting Month	Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
August – December 2005	0	0	NA
January – December 2006	0	0	NA
January – December 2007	0	0	NA
January 2008	0	0	NA

## 9.0 IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.01 AAJV has been implementing the required environmental mitigation measures according to the project Mitigation Implementation Schedule. The implementation schedule with mitigation measures is presented in the First Impact EM&A report.

9.02 A summary of environmental mitigation measures generally implemented by AAJV in this reporting month is presented as follows;

### Water Quality

- Wastewater were appropriately treated by treatment facilities;
- Drainage channels were provided to convey run-off into the treatment facilities;
- Drainage systems were regularly and adequately maintained.

### Landscaping

- Tree protection measures were provided to existing trees;
- No tree was unnecessarily lopped or felled.

### Air Quality

- Vehicles were cleaned of mud and debris before leaving the site;
- Site vehicles were limited to within 15 km/hr;
- Public roads around the site entrance/exit had been kept clean and free from dust;
- Dust suppression measures were properly provided to reduce dust emission from stockpile.

### Construction Noise

- Works and equipment were located to minimise noise nuisance from the nearest sensitive receiver;
- Idle equipments were either turned off or throttled down;
- Some of the Powered Mechanical Equipments were covered or shielded by appropriate acoustic materials if practicable.



Waste and Chemical Management

- Wastes were properly segregated into inert and non-inert in appropriate containers/areas;
- Excavated materials were reused where practicable.
- A chemical waste storage area had been provided on site;

General

- The site was generally kept tidy and clean.

## 10.0 IMPACT FORECAST

### KEY ISSUES FOR THE COMING MONTH

10.01 Key issues to be considered in the coming month include:

- Implementation of dust suppression measures at all times;
- Potential fugitive dust quality impact due to dry/windy season (November to March) from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Management of chemical wastes;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures.

10.02 The tentative 3-month rolling program is presented in **Appendix H**.

## 11.0 CONCLUSION

11.01 The EM&A program in **January 2008** was undertaken in compliance with the EM&A manual for the Peng Chau Sewage Treatment Works Upgrade. A summary of environmental compliance of air quality, construction noise and marine water quality in this reporting month are presented in **Table 11-1**.

**Table 11-1 Summary of the Exceedances for Impact Monitoring**

Env. Quality	Parameters	Compliance %	Investigation & Corrective Actions
Air Quality	1-Hour TSP	100	Not Required for 100% Compliance
	24-Hour TSP	100	Not Required for 100% Compliance
Noise	Leq (30min) Daytime	100	Not Required for 100% Compliance
Marine Water Quality*	-	-	-

Note: \* No marine water quality impact monitoring was required since all marine based construction activities were completed on 01 August 2006.

11.02 No Action/Limit Level exceedance of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

11.03 All noise levels measured at AN1 were below the Limit level and no complaint (Action Level) was received in this reporting month.

11.04 No marine water quality impact monitoring was required in this reporting month during the course of marine works was completed on 01 August 2006.

11.05 Based on the EM&A Manual Clause 4.32, the post marine water quality monitoring was carried out from 02 August 2006 to 01 September 2006. All the monitoring results in the control/impact stations were within the baseline range. The monitoring results and graphical plot were present in pervious Monthly EM&A Report (September 2006).

11.06 No environmental complaint or summons was received in this reporting month.

**RECOMMENDATIONS**

11.07 Based on the IEC site inspection records on 28 January 2008, the following key recommendations are pertinent:


- A 200L diesel oil drum oil located near the site entrance was not properly labeled. AAJV should properly label that oil drum;
- The Contractor was reminded to cover dusty stockpiles/materials including soil and sand after used;
- Drip trays were provided for the chemical containers to prevent soil contamination;
- The Contractor was reminded to cover the chemical containers by impervious sheet when not being used; and
- The Contractor was reminded to remove stagnant water after raining.


11.08 The ET will continue to implement the EM&A program and audit the implementation of the environmental mitigation measures.



## **Appendix A**

### **Project Site Layout**

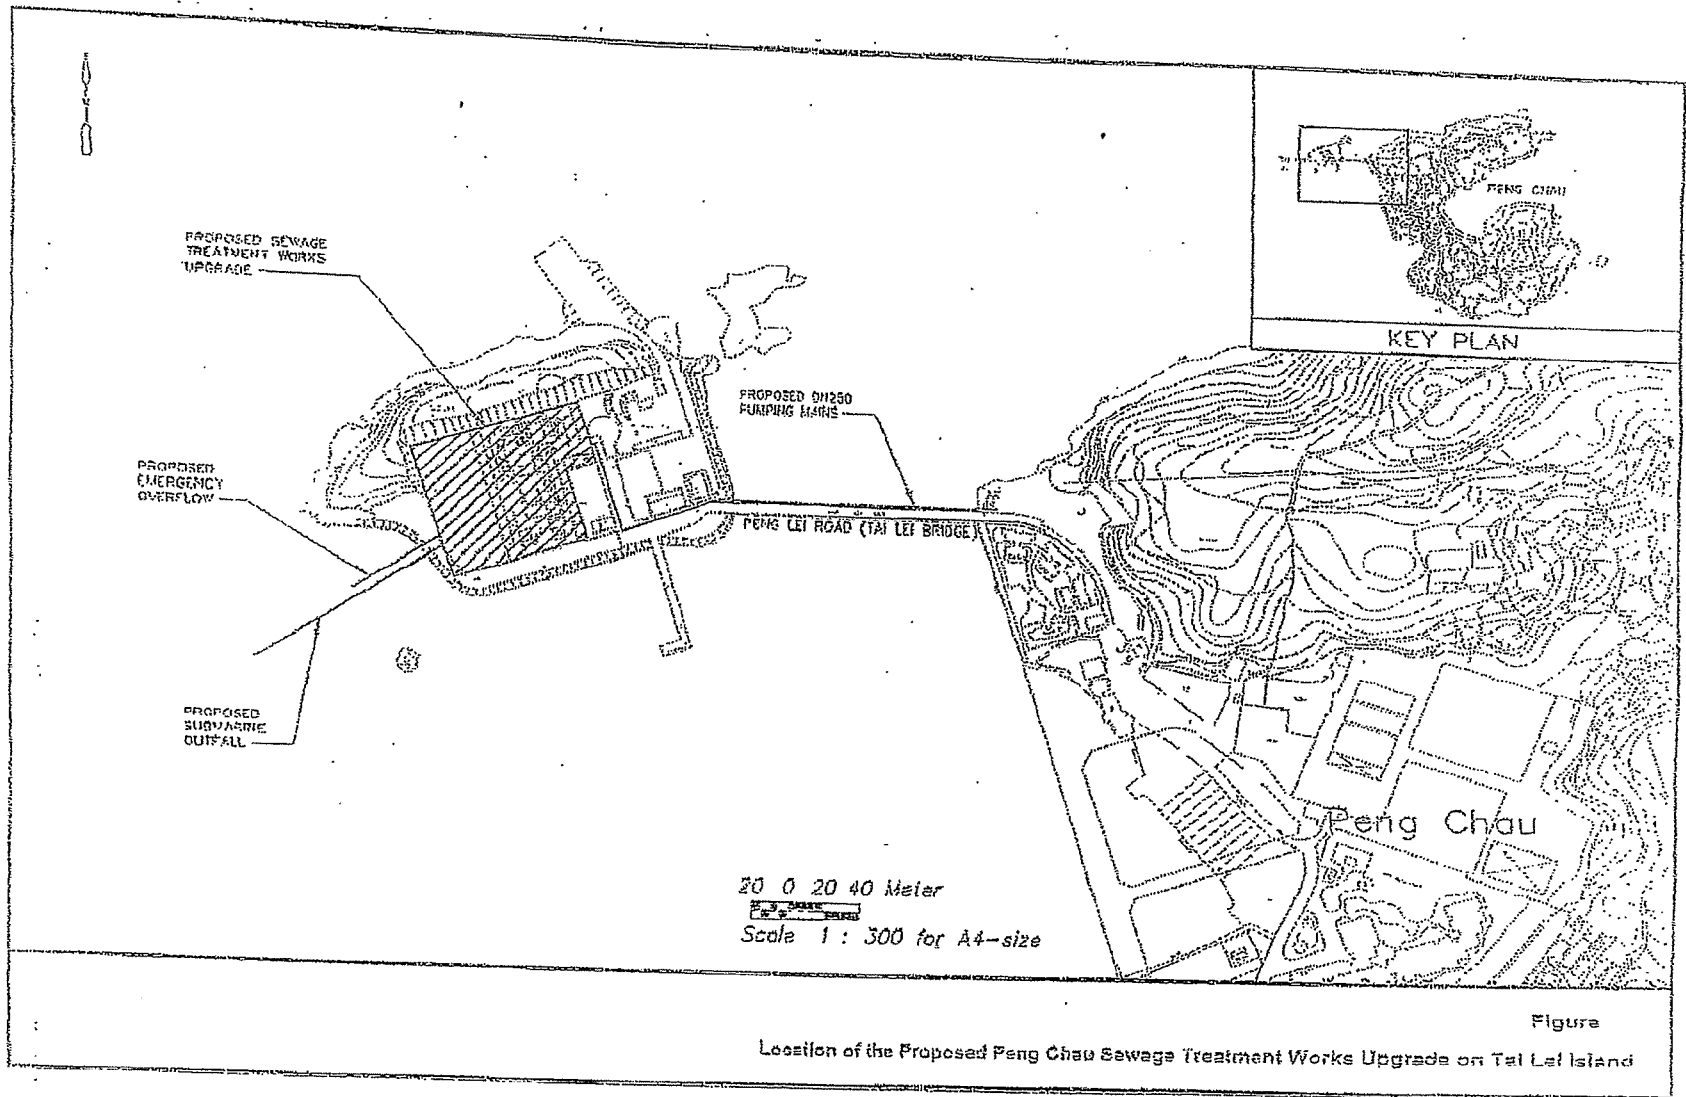

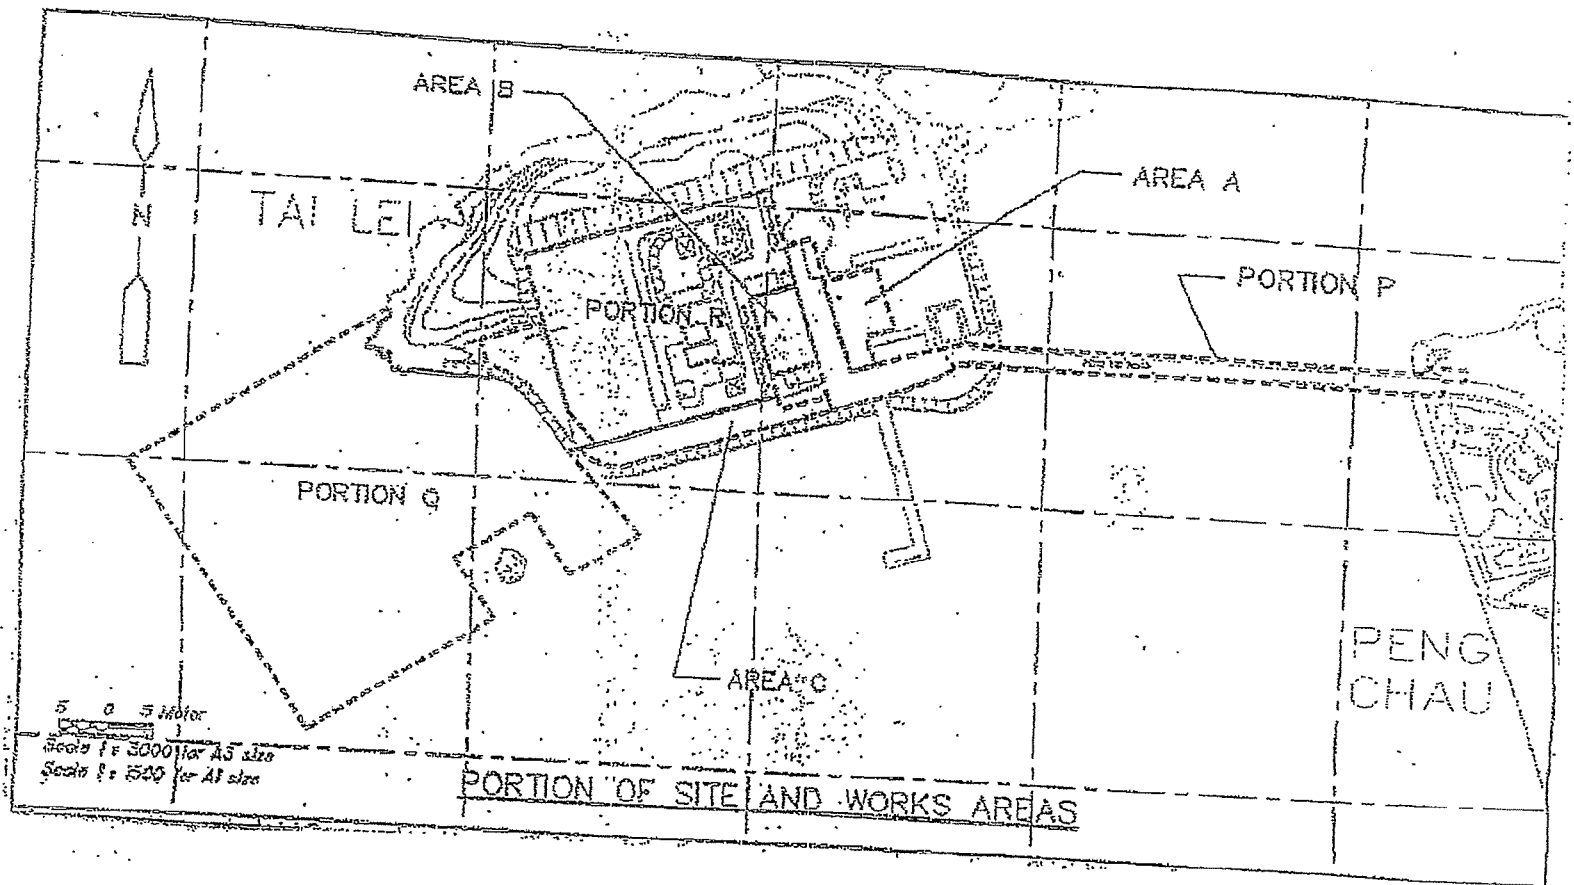

## **Appendix B**

### **Environmental Organization Structure**

**Contact Details of Key Personnel**

Organization	Project Role	Designation	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Permit Holder	Ir. David Leung	2594-7281	2827-8526
CDM	Engineer's Representative	Project Engineer	Ms. Angela Wong	2428-2332	2424-9114
		Resident Engineer	Mr. Alfred Cheung	2983-9303	2983-9843
		ARE	Mr. Alex Yeung	2983-9303	2983-9843
BMT Asia	Independent Environmental Checker	IEC	Mr. Antony Wong	2815-2221	2815-3377
		IEC'S Representative	Mr. Benny Ng	2815-2221	2815-3377
Acciona-ATAL	Main Contractor	Project Manager	Mr. William Chan	2983-0092	2983-0381
		Site Agent	To be Advised	2983-0092	2983-0381
AUES	Contractor's Environmental Team	Environmental Team Leader (ETL)	Mr. Ken Wong	2959-6059	2959-6079
		Project Supervisor	Mr. Benjamin Tam	2959-6059	2959-6079

## **Appendix C**

### **Locations of Designated Monitoring Stations**

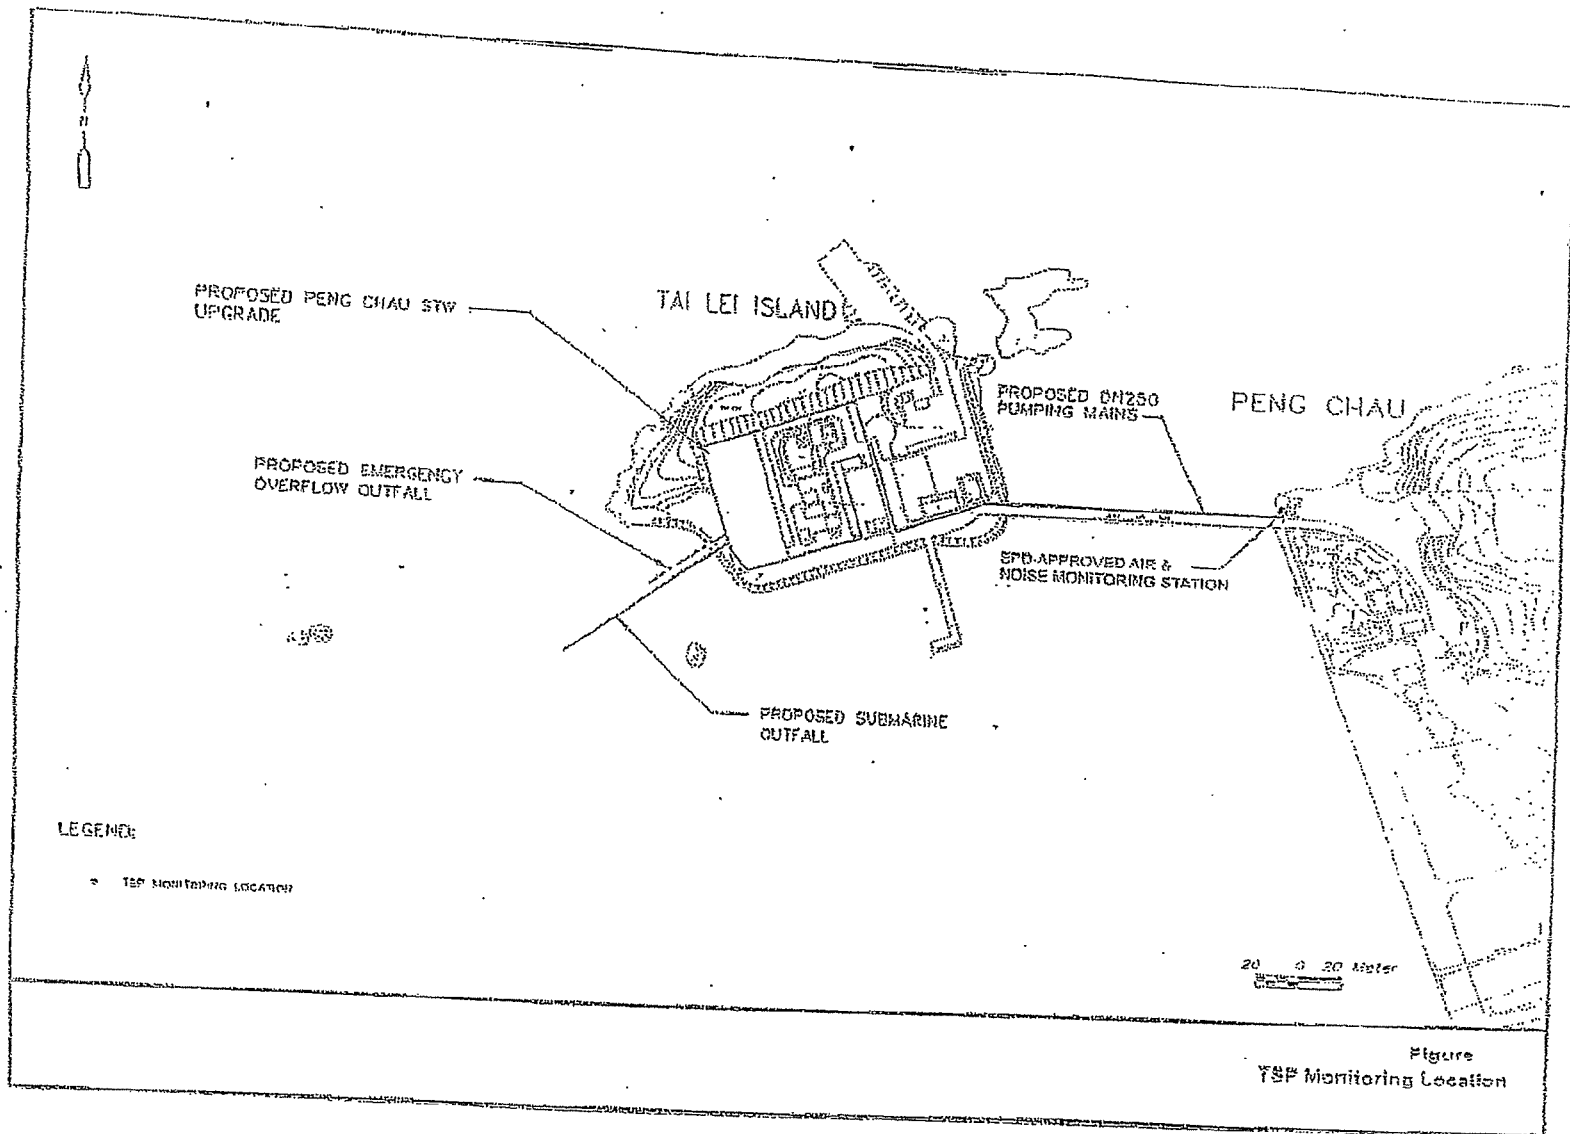


Figure  
TSP Monitoring Location

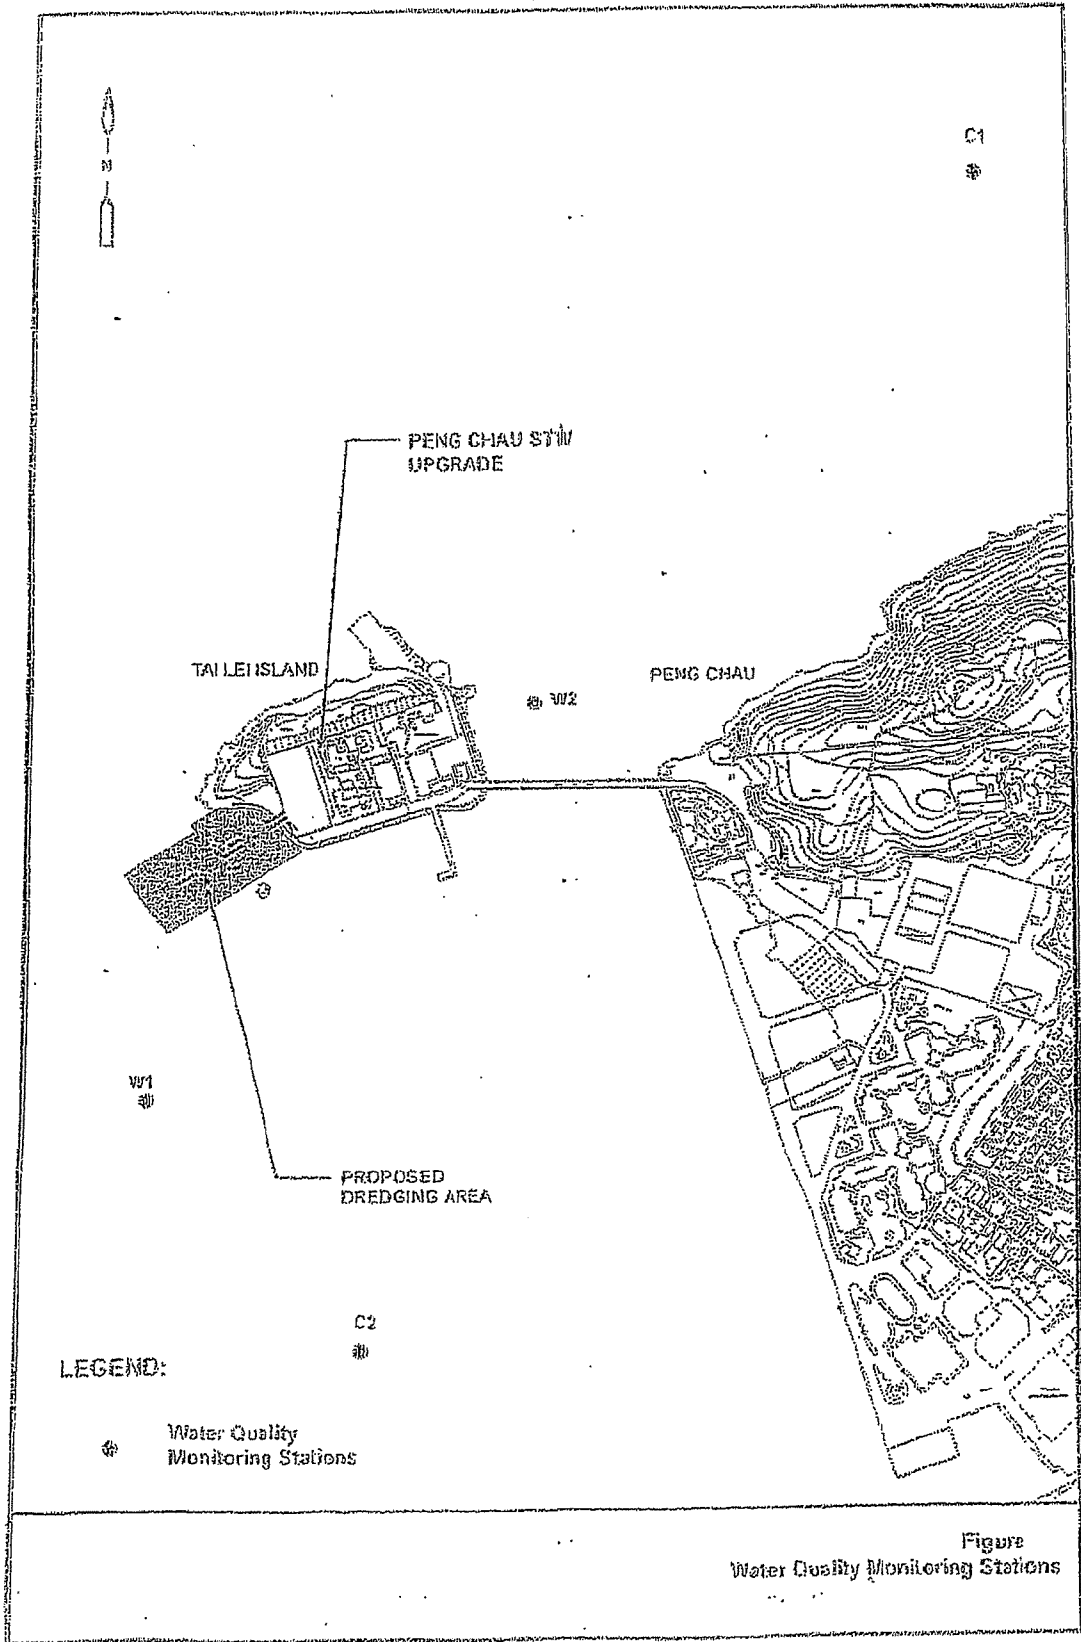


Figure  
Water Quality Monitoring Stations



## **Appendix D**

### **Equipment Calibration Certificates**

**Equipment Calibration List for Peng Chau Sewage Treatment Works Upgrade Project**

Item	Aspect	Description of Equipment	Serial No.	Date of Calibration	Date of Next Calibration
1	Air	Greasby Anderson GMWS2310 High Volume Sampler	AN1	07 Nov 07	07 Feb 08
2		Sibata LD-3	362337	25 Jun 07	25 Jun 08
3	Noise	Bruel & Kjaer 4231 Acoustical Calibrator	2292168	16 Apr 07	16 Apr 08
4		Bruel & Kjaer 2238 Integrating Sound Level Meter	2285721	16 Apr 07	16 Apr 08

Note:\* Calibration certificates will only be provided if monitoring equipment is re-calibrated or new.

*No marine water quality impact monitoring was required in this reporting period, since all marine based construction activities were completed on 01 August 2006. Post marine water quality monitoring was carried out from 02 August to 01 September 2006. Therefore, no water quality monitoring equipments calibration certificate was enclosed in this Monthly EM&A Report.*

## **Appendix E**

### **Impact Monitoring Schedules**

**Impact Monitoring Schedules in this Reporting Period**

Date		Dust Monitoring		Noise Monitoring
		1-Hour TSP	24-Hour TSP	
26-Dec-07	Wed			
27-Dec-07	Thu			
28-Dec-07	Fri			
29-Dec-07	Sat			
30-Dec-07	Sun			
31-Dec-07	Mon			
1-Jan-08	Tue			
2-Jan-08	Wed			
3-Jan-08	Thu			
4-Jan-08	Fri			
5-Jan-08	Sat			
6-Jan-08	Sun			
7-Jan-08	Mon			
8-Jan-08	Tue			
9-Jan-08	Wed			
10-Jan-08	Thu			
11-Jan-08	Fri			
12-Jan-08	Sat			
13-Jan-08	Sun			
14-Jan-08	Mon			
15-Jan-08	Tue			
16-Jan-08	Wed			
17-Jan-08	Thu			
18-Jan-08	Fri			
19-Jan-08	Sat			
20-Jan-08	Sun			
21-Jan-08	Mon			
22-Jan-08	Tue			
23-Jan-08	Wed			
24-Jan-08	Thu			
25-Jan-08	Fri			

*No Water Quality Monitoring was required in this reporting period, since all marine based construction activities were completed on 01 August 2006. Post Water Quality was carried out from 02 August to 01 September 2006, monitoring results were presented in the previous Monthly EM&A Report (September 2006)*

	Monitoring Day
	Sunday or Public Holiday




**Impact Monitoring Schedules in the Next Reporting Period**

Date		Dust Monitoring		Noise Monitoring
		1-Hour TSP	24-Hour TSP	
26-Jan-08	Sat			
27-Jan-08	Sun			
28-Jan-08	Mon			
29-Jan-08	Tue			
30-Jan-08	Wed			
31-Jan-08	Thu			
1-Feb-08	Fri			
2-Feb-08	Sat			
3-Feb-08	Sun			
4-Feb-08	Mon			
5-Feb-08	Tue			
6-Feb-08	Wed			
7-Feb-08	Thu			
8-Feb-08	Fri			
9-Feb-08	Sat			
10-Feb-08	Sun			
11-Feb-08	Mon			
12-Feb-08	Tue			
13-Feb-08	Wed			
14-Feb-08	Thu			
15-Feb-08	Fri			
16-Feb-08	Sat			
17-Feb-08	Sun			
18-Feb-08	Mon			
19-Feb-08	Tue			
20-Feb-08	Wed			
21-Feb-08	Thu			
22-Feb-08	Fri			
23-Feb-08	Sat			
24-Feb-08	Sun			
25-Feb-08	Mon			

	Monitoring Day
	Sunday or Public Holiday

## **Appendix F**

### **Graphical Plots of Air Quality and Construction Noise Monitoring Results**

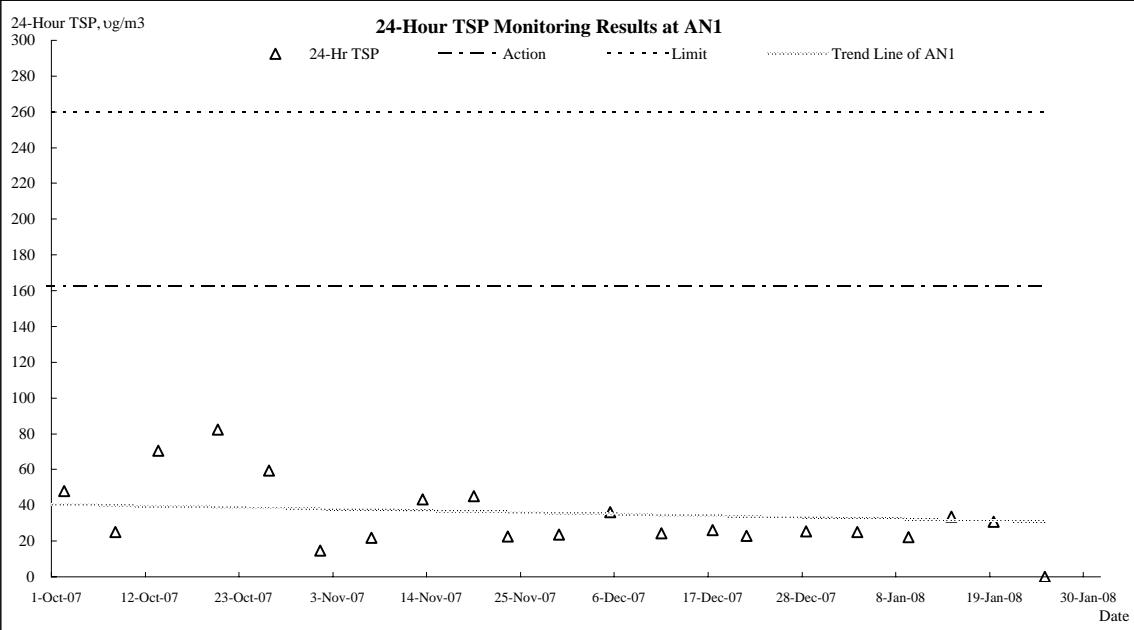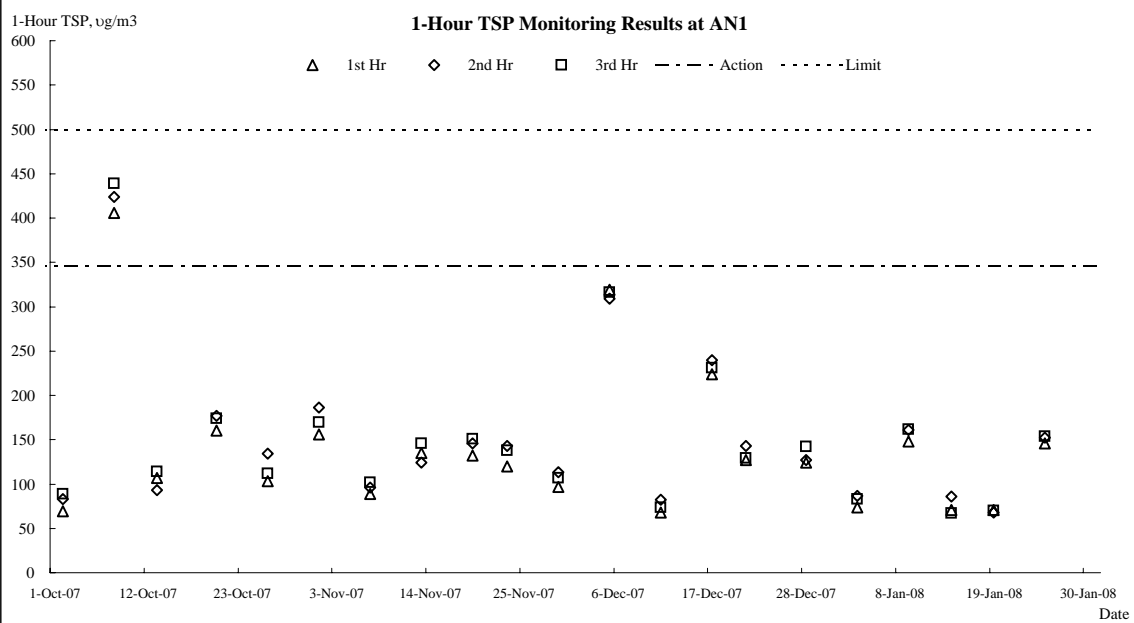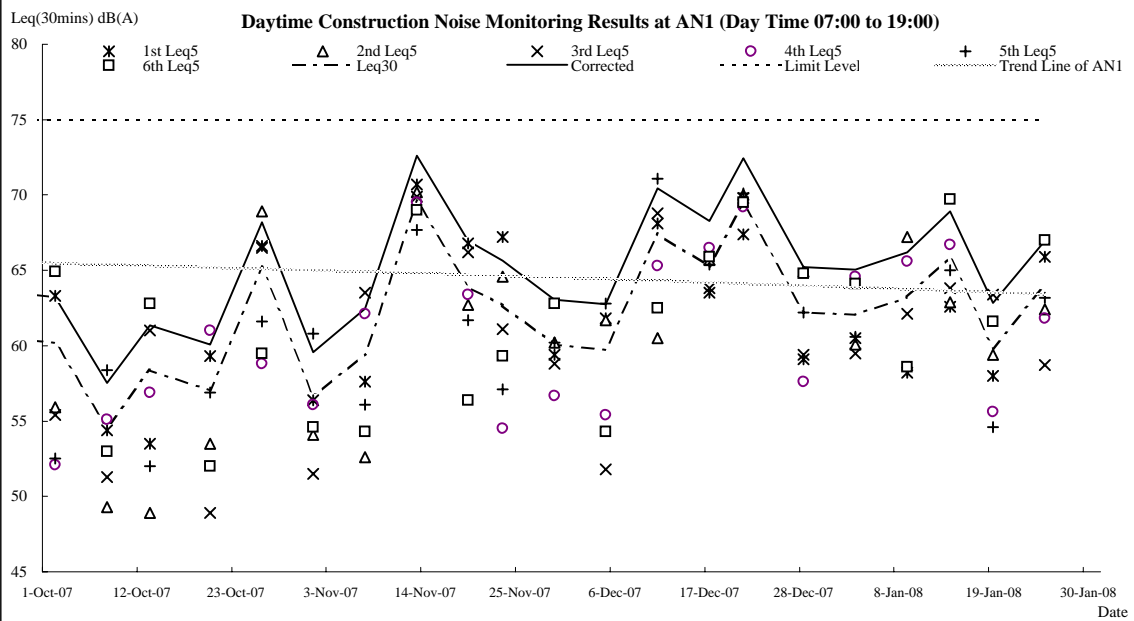

## **Appendix G**

### **Meteorological Data in the Reporting Period**




**Meteorological Data Extracted from HKO in the Reporting Period**

Date	Weather	Peng Chau Weather Station					
		Total Rainfall (mm)	Mean Air Temperature (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction	
26-Dec-07	Wed		Holiday				
27-Dec-07	Thu	fine/haze/moderate	0	18.9	18	72.5	E
28-Dec-07	Fri	fine/moderate/cloudy/cool	0	20.4	11.5	71.7	E/NE
29-Dec-07	Sat	cloudy/dry/sunny intervals/moderate/fresh	0	18.4	14.2	74	N/NE
30-Dec-07	Sun	fine/very dry/cold/fresh	0	16.3	20.7	41	N/NE
31-Dec-07	Mon	fine/very dry/cold/fresh	0	15	23.5	40	N/NE
1-Jan-08	Tue		Holiday				
2-Jan-08	Wed	cool/very dry/moderate	0	13.5	10	48	W/NW
3-Jan-08	Thu	fine/very dry/moderate	0	15.1	10	56	N/NW
4-Jan-08	Fri	fine/dry/haze/moderate/fresh	0	16.5	12.7	57.2	E/NE
5-Jan-08	Sat	fine/dry/haze/moderate	0	17.3	13.5	64.5	N/NW
6-Jan-08	Sun	fine/cool/very dry/moderate	0	19.3	10	48	S/SW
7-Jan-08	Mon	fine/cool/very dry/moderate	0	20.2	10	56	N/NW
8-Jan-08	Tue	cloudy/haze/sunny intervals/rain/moderate	Trace	21.1	12.7	69.2	E/NE
9-Jan-08	Wed	sunny periods/haze/cloudy/moderate	0	21.3	13	73.5	E/NE
10-Jan-08	Thu	cloudy/rain/moderate/fresh	Trace	20.9	20	76	E/NE
11-Jan-08	Fri	fog/sunny intervals/moderate	Trace	21.9	13.5	89	E/NE
12-Jan-08	Sat	fine/cloudy/foggy/moderate	0	22.6	8.2	84.5	S/SE
13-Jan-08	Sun	cloudy/rain/cool/dry/moderate/fresh	Trace	18.1	15	67	E/NE
14-Jan-08	Mon	cloudy/rain/cool/dry/moderate/fresh	Trace	15.1	27.5	66.5	N/NW
15-Jan-08	Tue	cloudy/rain/moderate/cold/fresh	0.7	14.3	18	69.2	N/NW
16-Jan-08	Wed	cloudy/rain/moderate/cold/fresh	Trace	14.3	29	61.5	N/NW
17-Jan-08	Thu	cloudy/cold/rain/moderate/fresh	Trace	12.1	23	61	N/NW
18-Jan-08	Fri	cloudy/sunny intervals/cool/moderate/fresh	Trace	14	16.5	75	N/NW
19-Jan-08	Sat	cloudy/fresh	Trace	16.5	28	77.5	E/NE
20-Jan-08	Sun	fine/hazy/cloudy/moderate	Trace	19	11.5	78	S/SE
21-Jan-08	Mon	fine/hazy/cloudy/moderate	Trace	21.9	26.2	76	NW
22-Jan-08	Tue	cloudy/haze/moderate	Trace	18.1	14.2	71	W/NW
23-Jan-08	Wed	cloudy/dry/haze/moderate	Trace	17.5	23	68.5	W/NW
24-Jan-08	Thu	cloudy/overcast/rain/cool/moderate	0.5	13.9	15	70	N/NW
25-Jan-08	Fri	cloudy/rain/cold/moderate	19.2	12	15.5	93	N/NW

## **Appendix H**

### **Three-Month Rolling Program**

Drainage Services Department  
 Contract No. DC/2004/08  
 Upgrading of Peng Chau Sewage Treatment Works  
 3-Months Rolling Programme (Jan 2008 to Apr 2008)

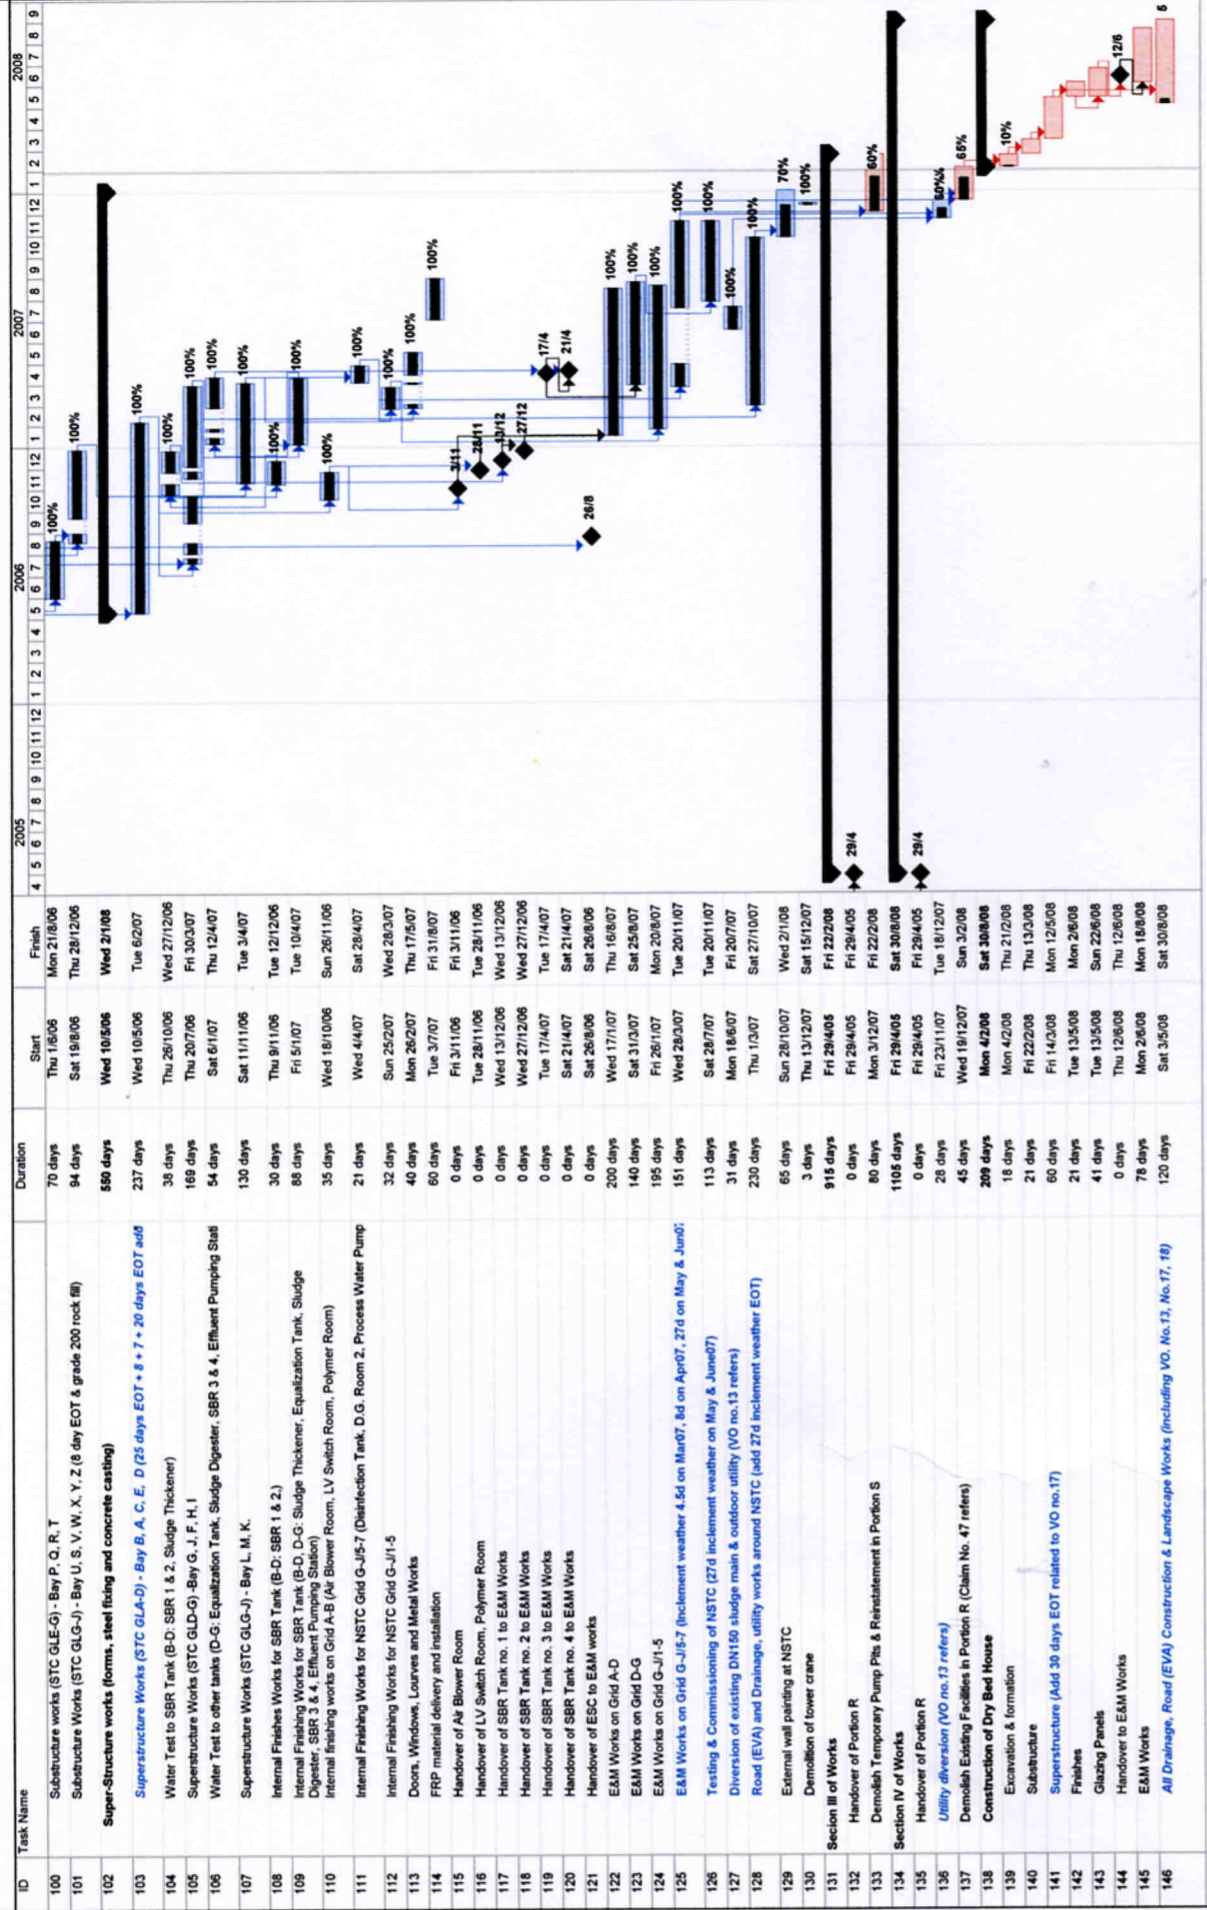

Project: Peng Chau-3months  
 Date: Tue 28/1/08

ACCIONA-ATAL JV

Legend:

- Task: Milestone (Blue), Summary (Red), Rolled Up Task (Black)
- Critical Task: (Red)
- Progress: (Blue)
- Spilt: (Red)
- External Tasks: (Grey)
- Project Summary: (Black)

Group By Summary

Page 3
