

Airport Management Services Limited

SkyCity Golf Course EM&A Monthly Impact Report

May 2006

8 June 2006

Report no: 01332R0041



Airport Management Services Limited

SkyCity Golf Course EM&A Monthly Impact Report

May 2006


Author: Adi LEE



Checker: Coleman Ng



Approver: Coleman NG



Report no: 01332R0041

Date:

8 June 2006

This report has been prepared for Airport Management Services Limited in accordance with the terms and conditions of appointment for Monthly Impact Report dated 10 March 2006. Hyder Consulting Ltd (COI Number 126012) cannot accept any responsibility for any use of or reliance on the contents of this report by any third party.

Hyder Consulting Ltd

COI Number 126012

47th Floor, Hopewell Centre, 183 Queens Road East, Wanchai, Hong Kong

Tel: +852 2911 2233 Fax: +852 2805 5028 www.hyderconsulting.com

Hyder

Consulting

Contents

1	Executive Summary	1
2	Site Audit.....	3
2.1	Water Quality	3
2.2	Air Quality	3
2.3	Noise	3
2.4	Waste/Chemical Management	4
2.5	Landscape and Visual	4
2.6	General.....	4
3	Marine Water Quality EM&A	5
3.1	Monitoring Results.....	5
3.1.1	Summary	5
3.1.2	Equipment and Methodology.....	6
3.1.3	Maintenance and Calibration.....	6
3.1.4	Parameters Monitored.....	7
3.1.5	Monitoring Locations	7
3.1.6	Monitoring Date, Time, Frequency and Duration	7
3.2	Action/Limit Levels.....	7
3.3	Summary of Exceedances.....	9
3.3.1	Review of Exceedances and Implications.....	9
3.3.2	Action Taken and Follow-up.....	9
3.4	Complaints and Notifications of Summons.....	9
3.4.1	Complaints.....	9
3.4.2	Notifications of Summons.....	9
3.5	Works Programme and Future Monitoring Schedule	9
4	Comments, Recommendations and Conclusions	11

Appendices

1	Site Audit Checklist
2	Marine Water Quality Monitoring Data
3	Equipment Calibration Details
4	Works Programme
5	Marine Water Monitoring Schedule for Next Month

Figures

- 1-1 Location of SkyCity Golf Course on the Airport Island
- 3-2 Location of Impact Monitoring Stations

Tables

- 3-1 Summary of Impact Monitoring Data
- 3-2 *In-situ* Monitoring Equipment Details
- 3-3 Monitoring Date, Time, Frequency and Duration
- 3-4 Action and Limit Levels
- 3-5 Event Action Plan for Marine Water Quality Monitoring

1 Executive Summary

The purpose of this Project is to construct and operate a 9-hole Golf Course at the east side of the North Commercial District (NCD) on the Airport Island as an interim arrangement prior to the area's future development as a business park (see Figure 1-1). The proposed interim golf facility, known as "SkyCity Golf Course" is intended to serve airport passengers, overseas visitors and airport workers until August 2013.

The Project will be managed by Airport Management Services Limited (AMS) who have employed a Works Contractor, Wing Fat Construction Co. Ltd., to carry out the construction works. Hyder Consulting have been employed as the Environmental Team (ET) for the Construction Period and have engaged ALS Technichem Pty Ltd as the HOKLAS accredited testing laboratory to carry out marine water analysis.

The construction work commenced on 7 March 2006 and it anticipated to last for a period of six to seven months. According to the approved EM&A Manual, impact monitoring during the Construction Period is required for suspended solids, dissolved oxygen and turbidity.

The monthly site audit revealed that there were no significant non-compliances in terms of water, air, noise, waste or landscape and visual, although the Environmental Team made a number of recommendations to the Works Contractor to improve environmental conditions.

Impact monitoring was carried out during May 2006 in accordance with the approved EM&A Manual. Monitoring was carried out on 1, 5, 9, 12, 15, 19, 22, 26 and 29 May. The monitoring results are detailed in this report, which complies with the reporting requirements stated in the approved EM&A Manual.

There were no exceedances of A/L Levels for the water quality monitoring.

There were no complaints received and no notifications of summons.

Overall, there are no adverse environmental impacts caused by the Works during the reporting month, although there is room for improvement in overall site environmental management – recommendations have been made and will be followed up in due course.

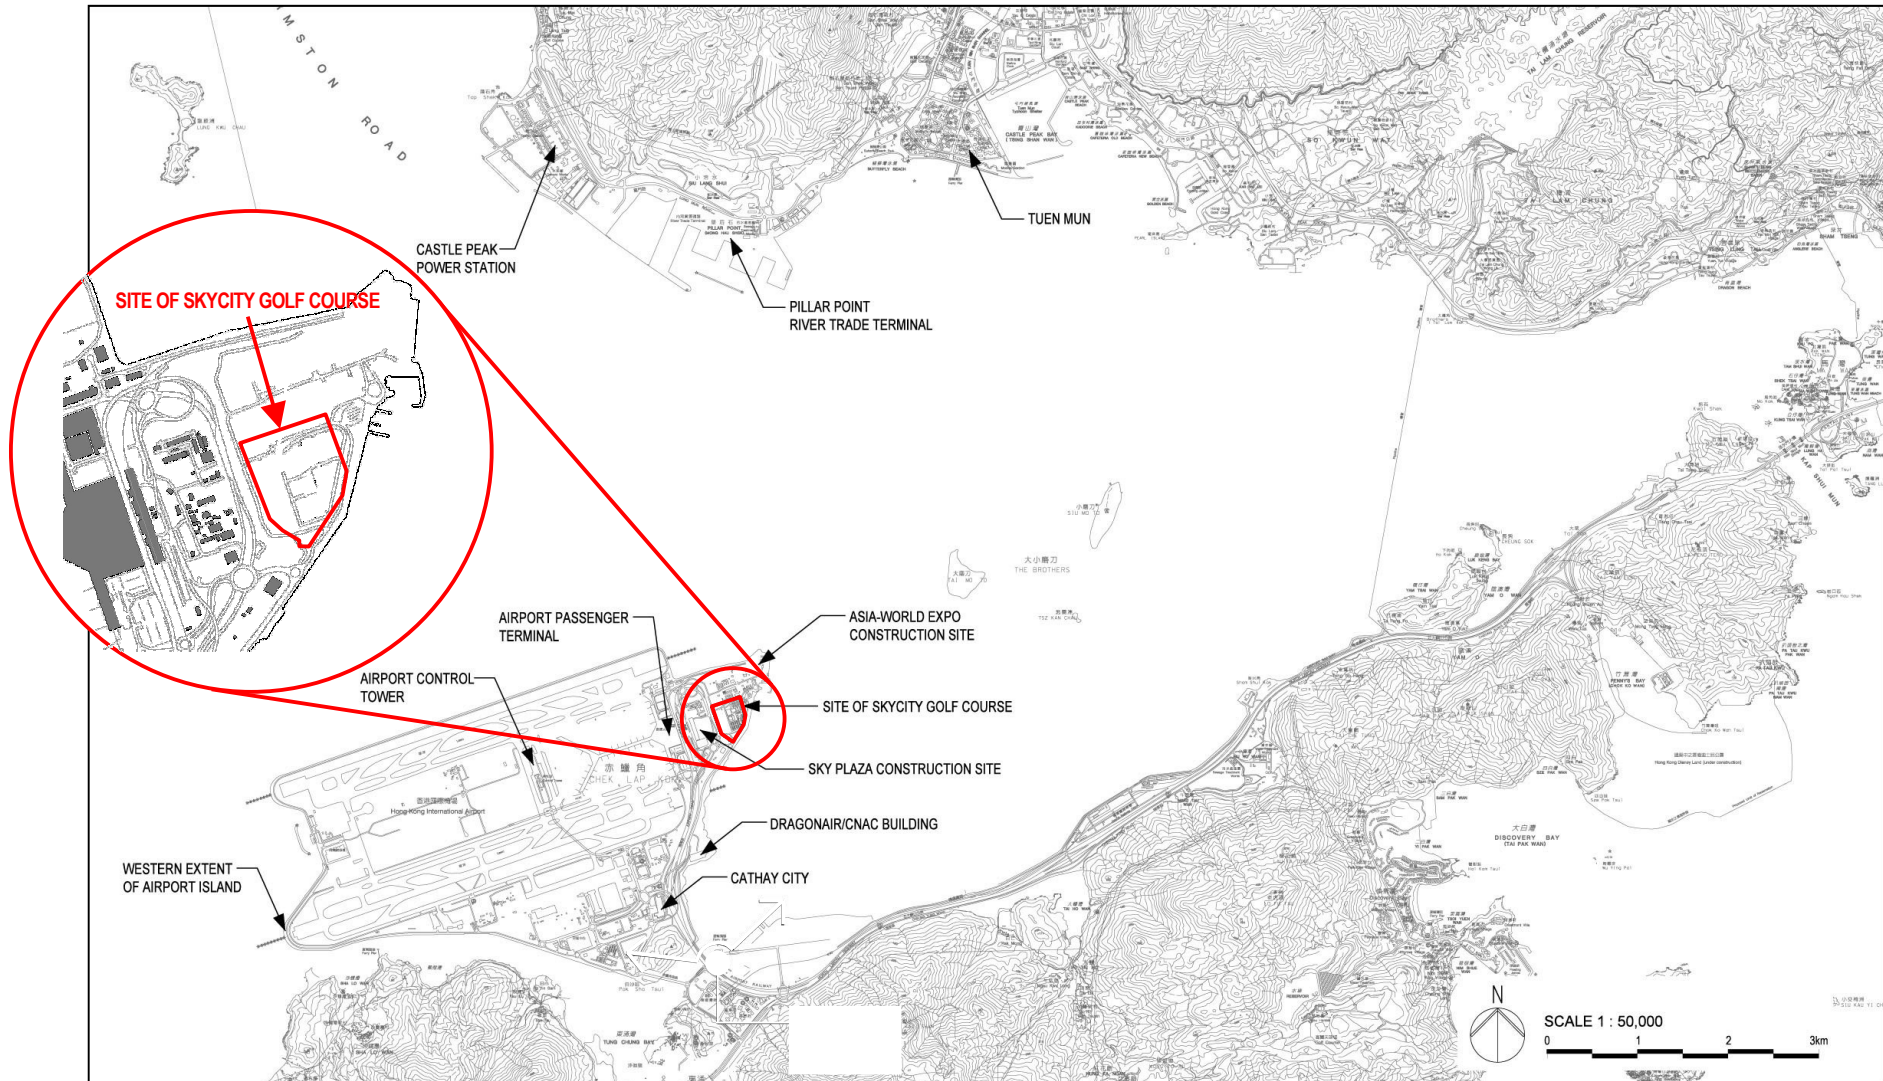


Figure 1-1 Location of SkyCity Golf Course on the Airport Island

2 Site Audit

The monthly site audit examines the implementation status of environmental protection, mitigation and pollution control measures.

Appendix 1 contains the site audit checklist for May 2006. From this the following observations on the implementation status of environmental, mitigation and pollution control measures can be made. Areas for improvement and follow-up are indicated on the checklist and have been highlighted below. The Works Contractor is aware of any shortcomings and has been advised by the ET of any improvements that are required.

2.1 Water Quality

A vehicle wheelwash has been provided at the site egress point. However, the Contractor was reminded to replace the muddy water in the wheel washing bay by clean water frequently. Perimeter U-channels have been completed around most of the site, however, some 20m along the southern part of the site remains to be completed. The Contractor was urged to complete the perimeter drainage.

As indicated by the Contractor, no water has been discharged from the site during the reporting month and it is intended that during forthcoming wet weather, water will be collected in the excavated lake bowls and from there percolate down to replenish the groundwater below the site. Because of this, it is not anticipated that there will be any surface runoff from the site.

It is noted that a Discharge Licence under the Water Pollution Control Ordinance has been issued by EPD to the Contractor. The Contractor is reminded to keep the license on site for inspection. The Contractor has also been reminded to make silt traps/settlement tanks available on site in case these are needed for discharge off-site.

2.2 Air Quality

It was observed that the unpaved areas and haul roads were watered except for a small part of the site. The Contractor was reminded to provide watering to all dry unpaved areas and haul roads. The Contractor provided water spraying to such areas immediately during the site inspection.

Dust was emitted during rock breaking. The Contractor has been reminded to provide water spraying during breaking activities.

2.3 Noise

No significant noise problems were noted. The most apparent noise source is overhead aircraft.

2.4 Waste/Chemical Management

Three-colour recycling bins have been placed near to the Contractor's site office. The Contractor has registered as a Waste Producer under the Waste Disposal Ordinance. It was observed that chemical waste storage has been provided.

All diesel storage tanks and oil/lubricant drums have been provided with a drip tray. However, some empty oil drums on bare ground were observed during the site inspection. The Contractor has been reminded to put the oil drums at proper place such as chemical waste storage.

2.5 Landscape and Visual

The site is completely surrounded by a hoarding and there are no landscape or visual issues at this time.

2.6 General

The Environmental Permit is displayed at the entrance to the site as required. Although the Contractor has applied and/or received other permits and licences relating to environmental protection, these are not filed in an accessible manner. The Contractor was recommended to ensure that all relevant permits and licences are easily available for inspection, by both the ET and also by EPD.

Overall, the site operation is acceptable from an environmental point of view, but there is room for improvement. The Contractor has been advised of those areas which require immediate attention and this will be followed-up during the next site audit.

3 Marine Water Quality EM&A

Monitoring of Dissolved Oxygen (DO) concentration in mg/l, Suspended Solids (SS) in mg/l and turbidity in NTU, was carried out by the ET to ensure that any deterioration in marine water quality could be readily detected and timely action could be taken to rectify the situation if this was due to site activities. DO and turbidity were measured *in-situ* whilst SS was determined in laboratory.

Other parameters, such as water depth, sea temperature, salinity and DO saturation are recorded for reference, and weather conditions, sea conditions, tidal stage and any particular site activities are recorded for information.

3.1 Monitoring Results

3.1.1 Summary

A summary of monitoring results for the reporting month is provided in Table 3-1, below. Detailed results are provided in Appendix 2, in which exceedances of Action/Limit (A/L) Levels are highlighted.

Station		Temperature (°C)	Salinity (mg/ℓ)	DO Saturation (%)	DO Concentration (mg/ℓ)	Turbidity (NTU)	SS (mg/ℓ)
C1	Mean	26.1	23.2	94.3	6.7	5	5
	Maximum	27.6	27.9	102.8	7.2	12	11
	Minimum	25.3	13.6	84.3	6.0	1	2
C2	Mean	25.9	24.5	97.2	6.9	4	6
	Maximum	26.8	28.0	119.2	8.4	10	14
	Minimum	25.1	19.5	85.1	5.9	2	3
M1	Mean	26.0	24.5	95.7	6.8	5	5
	Maximum	27.6	27.8	103.7	7.4	9	13
	Minimum	25.2	16.8	84.9	5.9	2	3
M2	Mean	26.0	24.2	96.6	6.8	5	5
	Maximum	27.8	27.8	112.4	8.1	9	8
	Minimum	25.1	16.7	84.7	5.9	2	3

Table 3-1 Summary of Impact Monitoring Data

3.1.2 Equipment and Methodology

Because of the relatively shallow water, *in-situ* measurements and water sampling were conducted at only one water depth – the mid-depth. Water samples for all monitoring parameters were collected, stored, preserved and analysed according to *APHA Standard Methods for the Examination of Water and Wastewater, 19th Edition, #17*.

In-situ DO concentration, turbidity (and temperature, salinity and DO saturation) were carried out using a YSI Model 6820 CE-C-M-Y multi-parameter meter:

Parameter	YSI Model 6820 CE-C-M-Y		
	Range	Resolution	Accuracy
DO Concentration	0 to 50 mg/l	0.01 mg/l	0 to 20 mg/l: $\pm 2\%$ of reading or 0.2 mg/l, whichever is greater; 20 to 50 mg/l: $\pm 6\%$ of reading
DO Saturation	0 to 500%	0.1%	0 to 200%: $\pm 2\%$ of reading or 2% air saturation, whichever is greater; 200 to 500%: $\pm 6\%$ of reading
Turbidity	0 to 1,000 NTU	0.1 NTU	$\pm 2\%$ of reading or 0.3 NTU, whichever is greater
Temperature	-5 to +70°C	0.01°C	$\pm 0.15^\circ\text{C}$
Salinity	0 to 70 ppt	0.01 ppt	$\pm 1\%$ of reading or 0.1 ppt, whichever is greater

Table 3-2 *In-situ* Monitoring Equipment Details

A Kahlisco water sampler was used to obtain the water sample for subsequent SS analysis. Water samples were collected in high density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS' laboratory (HOKLAS accredited) immediately after completion of monitoring. The analysis follows *APHA Standard Methods #2540D*.

A Global Positioning System (GPS) was used to determine the exact monitoring location and water depth was determined using an echo-sounder.

3.1.3 Maintenance and Calibration

All *in-situ* monitoring instruments are calibrated and certified by ALS at 3-monthly intervals throughout the marine water quality monitoring programme.

For DO, the probe (YSI 6820) is calibrated once per monitoring day by the wet bulb method. Calibration at ALS is carried out once every three months in a water sample of known dissolved oxygen concentration. The sensor is immersed in the water and after thermal equilibration, the known mg/l value is keyed in and the calibration is carried out automatically.

For turbidity, the probe (YSI 6820) is calibrated with a solution of known NTU at ALS once every three months. Calibration as per dissolved oxygen, above.

Calibration details are provided in Appendix 3.

3.1.4 Parameters Monitored

The following parameters are monitored and compared to A/L Levels:

- Dissolved Oxygen (DO)
- Suspended Solids (SS)
- Turbidity

Other parameters, such as water depth, sea temperature, salinity and dissolved oxygen saturation were recorded for reference, and weather conditions, sea conditions, tidal stage and any particular site activities were recorded for information.

3.1.5 Monitoring Locations

Monitoring locations together with grid references are shown in Figure 3-2. Control Stations are designated C1 and C2 and Monitoring Stations are designated M1 and M2.

3.1.6 Monitoring Date, Time, Frequency and Duration

Monitoring of marine water quality is carried out twice-weekly during mid-ebb and mid-flood tides. Table 3-3, below, provides details of the monitoring dates, times and duration:

Date	Duration of Ebb Tide	Monitoring at Mid-Ebb	Duration of Flood Time	Monitoring at Mid-Flood
1/5/06	13:23 to 17:23	15:23	06:10 to 10:10	08:10
5/5/06	16:48 to 20:48	18:48	04:15 to 08:15	06:15
8/5/06	08:36 to 12:36	10:36	14:00 to 18:00	16:00
12/5/06	10:30 to 14:30	12:30	17:10 to 21:10	19:10
15/5/06	12:15 to 16:15	07:15	05:15 to 09:15	07:15
19/5/06	15:33 to 19:33	17:33	03:03 to 07:03	05:03
22/5/06	07:29 to 11:29	09:29	12:43 to 16:43	14:43
26/5/06	10:19 to 14:19	12:19	17:07 to 21:07	19:07
29/5/06	12:26 to 16:26	14:26	05:08 to 09:08	07:08

Table 3-3 Monitoring Date, Time, Frequency and Duration

3.2 Action/Limit Levels

The A/L Levels for the impact monitoring stations (M1 and M2) were determined in the approved Interim Baseline Monitoring Report and are shown in Table 3-4:

Parameter	Action Level	Limit Level
DO Concentration	5 th percentile of baseline data = 7.0 mg/l, or 80% of the upstream control station	4.0 mg/l, or 70% of the upstream control station
Turbidity	95 th percentile of baseline data = 9.6 NTU, or 120% of the upstream control station	99 th percentile of baseline data = 10.5 NTU, or 130% of the upstream control station
SS	95 th percentile of baseline data = 9.4 mg/l, or 120% of the upstream control station	99 th percentile of baseline data = 9.9 mg/l, or 130% of the upstream control station

Table 3-4 Action and Limit Levels for Water Monitoring Stations

In case of exceedance of A/L Levels at M1 or M2, the Event/ Action Plan (shown in Table 3-5, below) shall be followed.

Event	Action	
	ET	Works Contractor
Exceedance of Action Level	<ol style="list-style-type: none"> 1. Identify the source(s) of impact. If not from the Project then provide justification and document this 2. If exceedance is caused by the Project then inform Contractor 3. Check monitoring data and Contractor's working methods 4. Discuss possible mitigation measures with Contractor 5. Repeat measurement on next day of exceedance 	<ol style="list-style-type: none"> 1. Confirm notification of the exceedance in writing 2. Rectify any unacceptable practice 3. Check all plant and equipment 4. Amend working methods if appropriate 5. Discuss possible mitigation measures with ET 6. Implement the agreed mitigation measures
Exceedance of Limit Level	<ol style="list-style-type: none"> 1. Identify the source(s) of impact. If not from the Project then provide justification and document this in the EM&A Report 2. If exceedance is caused by the Project then inform Contractor 3. Check monitoring data and Contractor's working methods 4. Agree mitigation measures with Contractor 5. Ensure mitigation measures are implemented immediately 6. Increase the monitoring frequency to daily until no further exceedance of Limit Level 	<ol style="list-style-type: none"> 1. Confirm notification of the exceedance in writing 2. Rectify any unacceptable practice 3. Check all plant and equipment 4. Amend working methods if appropriate 5. Agree possible mitigation measures with ET 6. Implement the agreed mitigation measures immediately

Table 3-5 Event Action Plan for Marine Water Quality Monitoring

3.3 Summary of Exceedances

3.3.1 Review of Exceedances and Implications

There were no exceedances of A/L Levels for the water quality monitoring during May 2006.

3.3.2 Action Taken and Follow-up

As no exceedance of A/L Levels were recorded during the reporting month, no action or follow-up is deemed to be necessary.

3.4 Complaints and Notifications of Summons

3.4.1 Complaints

No complaints were received during the reporting month and there are no outstanding follow-up issues to be addressed.

3.4.2 Notifications of Summons

No notifications of summons were received during the reporting month and there are no outstanding follow-up issues to be addressed.

3.5 Works Programme and Future Monitoring Schedule

Appendix 4 shows the current work programme for the works and Appendix 5 provides the future schedule for marine water quality monitoring.

Based on the work to be carried out in future months, no significant impacts to marine water quality are anticipated.

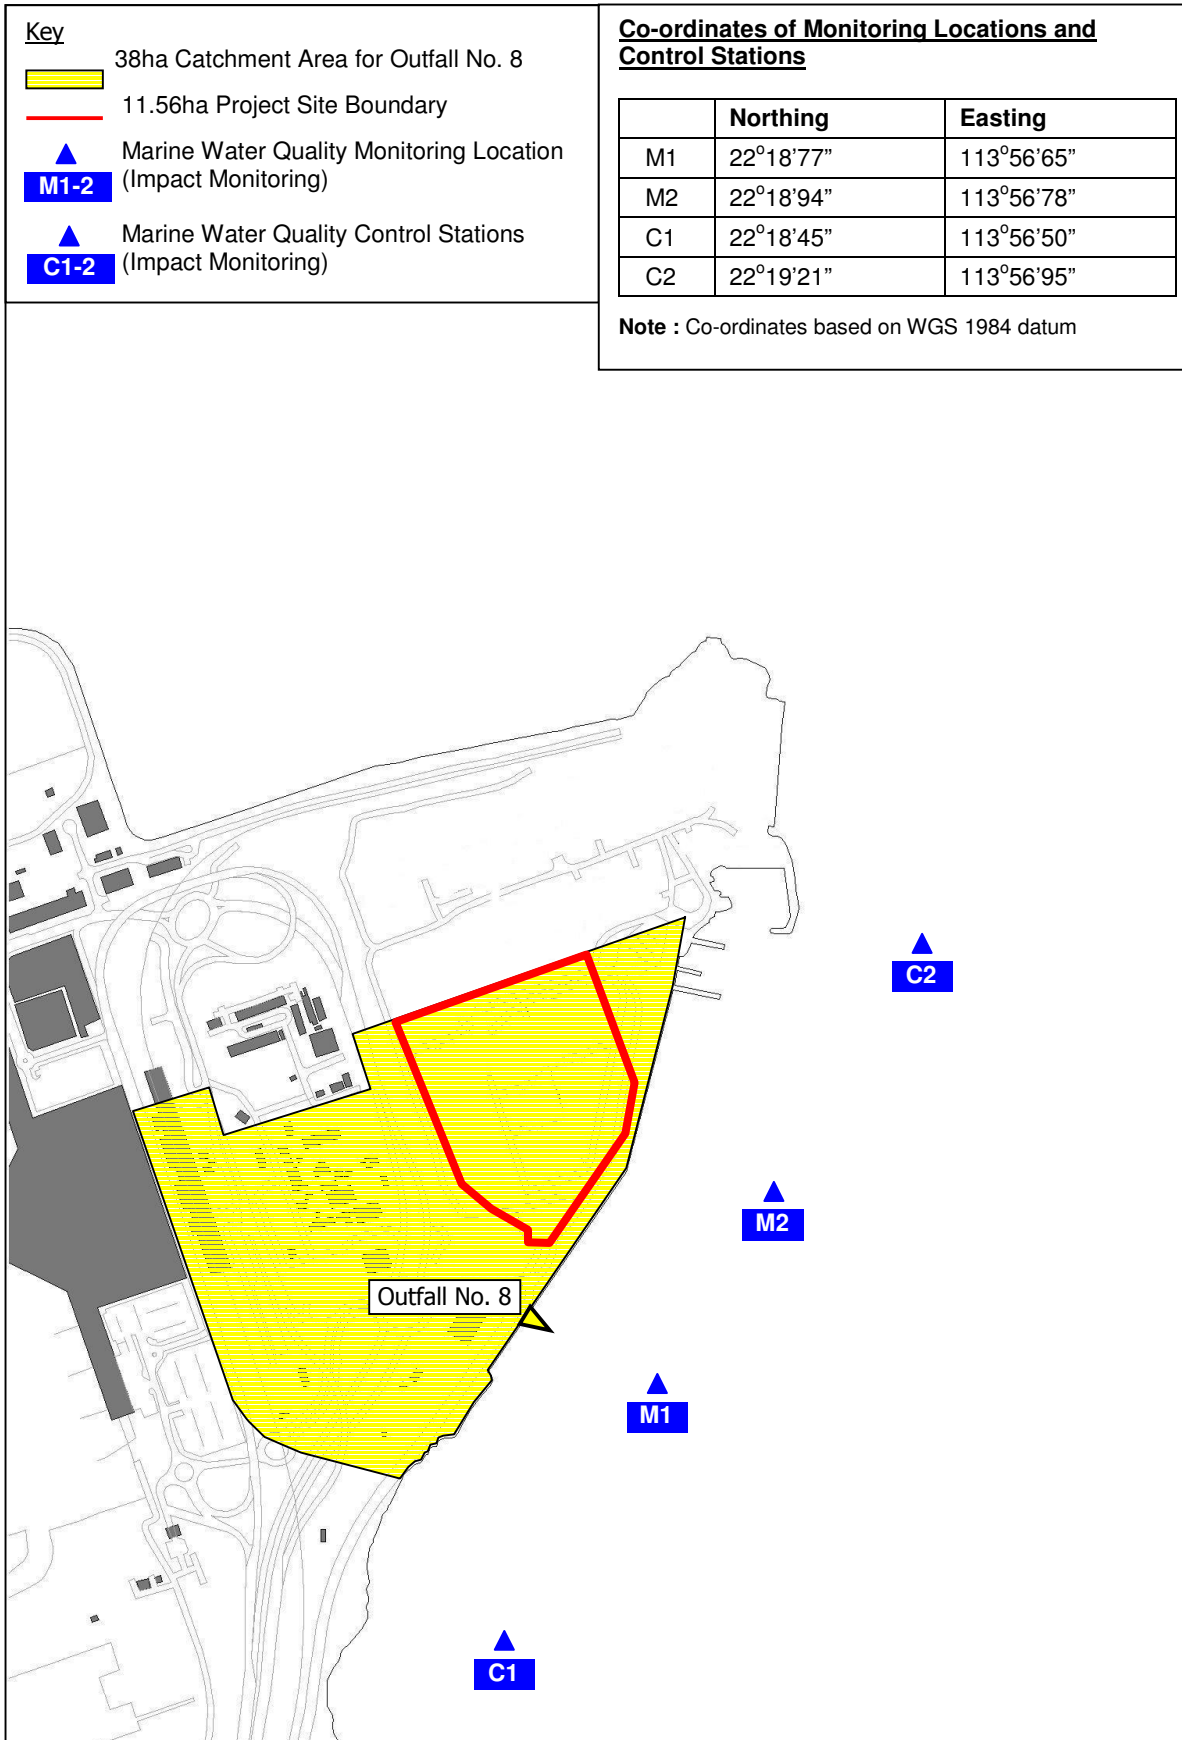


Figure 3-2 Location of Impact Monitoring Stations

4 Comments, Recommendations and Conclusions

The monthly site audit revealed that there were no significant non-compliances in terms of water, air, noise, waste or landscape and visual, although the Environmental Team made a number of recommendations to the Works Contractor to improve environmental conditions.

In terms of marine water quality monitoring, there were no exceedances of A/L Levels during May 2006.

There were no complaints received and no notifications of summons.

Overall, there are no adverse environmental impacts caused by the Works during the reporting month, although there is room for improvement in overall site environmental management – recommendations have been made and will be followed up in due course.

Appendix 1

Site Audit Checklist

SkyCity Golf Course
Environmental Team (ET) for Construction Period
SITE INSPECTION/AUDIT CHECKLIST



Inspection No.

Inspection Date 12-5-06 Time 10:00-11:00 am. Inspected By Client: Nil
Contractor: Honey
ET: Tony Naji

Site SkyCity Golf
Course Contractor Wing Fort

Weather

Condition Sunny Fine Overcast Drizzle Rain Storm Hazy

Temperature 29 °C Humidity High Moderate Low

Wind Calm Light Breeze Strong Direction E

	N/A or not observed	Yes	No	Photo/Remarks
1 Water Quality				
1.1 Perimeter cut off drains direct off-site water around the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	①
1.2 Is all surface runoff directed to silt removal facilities prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.3 Channels, earth bunds or sandbags direct surface runoff to silt removal facilities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.4 Is groundwater pumped out from tunnelling and excavations discharged via silt removal facilities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.5 Are there silt removal facilities for settling surface runoff prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.5.1 Constructed from pre-formed individual cells or silt traps / basins?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.5.2 Adequate capacity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.5.3 Free from silt and sand?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.5.4 Inspected and maintained after rain storm?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.6 Is drainage system well maintained to prevent flooding and overflow?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.7 Is exposed earth stabilized after earthworks have been completed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.8 Are exposed slope surfaces covered (by tarpaulin or other means)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.9 Are open stockpiles of excavated and construction materials covered during rainstorms?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.10 Any measures to prevent the washing away of excavated and construction materials e.g. sand/silt to drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.11 Are manholes covered and sealed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12 Are vehicles and plant cleaned of earth, mud and debris before leaving the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.13 Are vehicle washing facilities provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

SkyCity Golf Course
Environmental Team (ET) for Construction Period
SITE INSPECTION/AUDIT CHECKLIST



	N/A or not observed	Yes	No	Photo/Remarks
1.13.1 Wastewater treated in silt removal facility? Silt removal facility emptied of silt regularly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13.2 Washing area and road exiting from washing facility paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.13.3 Access road has sufficient backfall toward washing facility or bunded to prevent of untreated wastewater?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.14 Equipment oil and lubrication replacements performed only in bunded maintenance area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15 Drainage from maintenance area discharged via an oil interceptor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15.1 Oil and grease removed regularly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16 Toilets that connect to foul sewer or chemical toilets provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.17 Is debris and rubbish prevented from entering drains?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.18 Is Effluent Discharge Licence available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	(9)

2 AIR QUALITY

2.1 Are hoarding not less than 2.4m tall provided beside roads or areas with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2 Are the roads and unpaved areas watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	(3)
2.3 Are stockpiles of excavated material covered or regularly watered?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4 Is stockpile of dusty materials kept to not extend beyond the pedestrian barriers, fencing or traffic cones?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.5 Is the public road around the site entrance kept clean and free from dust?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6 Do the site vehicles use the vehicle wash facility at the site exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7 Are materials transported on trucks covered?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8 Are dusty materials sprayed prior to loading?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.9 Are all truck loads to a level within the side and tail boards?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.10 Are areas where demolition/site clearance/breaking take place regularly watered?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	(12)
2.11 Is every stock of more than 20 bags of cement or day covered entirely by impervious sheeting or placed in an area sheltered on the top and the three sided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12 Are potentially dusty demolished items/debris covered or placed in a three sided shelter?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12.1 Is the debris sprayed with water/dust suppression chemical to keep wet before it is dumped onto a debris chute?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.13 Odorous materials immediately covered and promptly removed from site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14 Are there enclosures around the main dust-generating activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

SkyCity Golf Course
Environmental Team (ET) for Construction Period
SITE INSPECTION/AUDIT CHECKLIST



Consulting

	N/A or not observed	Yes	No	Photo/Remarks
2.15 Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16 Are completed earthworks sealed and hydroseeded and planted as soon as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17 Are vehicles and equipment switched off while not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.18 Do vehicles and equipment maintained that no excessive smoke or visible vapour emitted?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Observable dust sources

<input checked="" type="checkbox"/> Wind erosion	<input checked="" type="checkbox"/> Vehicle/equipment movements
<input type="checkbox"/> Loading/unloading of materials	<input type="checkbox"/> Others _____

3 Noise

3.1 Are the construction works scheduled to minimise noise nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2 Are the works or equipment sited to minimize noise nuisance? Mobile plant sited away from NSRs? Noisy plant oriented away from NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3 Are all plant and equipment well maintained and in good operating condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4 Is idle equipment turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5 Are powered mechanical equipment covered or shielded by appropriate acoustic materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6 Are quiet plant used as required?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7 Are silencers/mufflers fitted and maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8 Are mobile/temporary noise barriers used where specified?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9 Do air compressors ($\geq 500\text{kPa}$ of supplying compressed air) and hand held percussive breakers ($>10\text{kg}$ in weight) have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10 Do compressors and generators operate with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.11 Are Construction Noise Permits available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Major noise source(s)

<input type="checkbox"/> Traffic	<input type="checkbox"/> Construction activities inside of site
<input checked="" type="checkbox"/> Construction activities outside of site	<input checked="" type="checkbox"/> Others <u>Aeroplane</u>

4 Waste/Chemical Management

4.1 General refuse

4.1.1 Accumulation on-site avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.1.2 Receptacles (e.g. rubbish bins) available?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.1.3 Disposed of regularly and properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	(13)
4.1.4 Records of quantities generated/recycled/disposed maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

SkyCity Golf Course
Environmental Team (ET) for Construction Period
SITE INSPECTION/AUDIT CHECKLIST



	N/A or not observed	Yes	No	Photo/Remarks
4.2 Chemical waste				
4.2.1 Stored properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.2.2 Storage in accordance with Code of Practice?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	6
4.2.3 Disposed of properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2.4 Trip tickets available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.3 Chemical/fuel storage				
4.3.1 Is storage area bunded?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.3.2 Adequate bund capacity? (>110% of the largest tank)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.3.3 Area storage area provided with locks and located on sealed areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.3.4 Are oil/fuel drums and plant/equipment provided with drip trays to prevent soil contamination?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.4 C&D Material				
4.4.1 Reused/recycled where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.4.2 Inert/non inert materials segregated?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.4.3 Disposed of properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.4.4 Records of quantities generated/recycled/disposed maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5 Excavated Material				
4.5.1 Reused where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5.2 Records of quantities generated/reused/disposed maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6 Are spent bentonite slurries or grouts collected, reconditioned and reused?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7 Is foam, oil, grease, litter or other objectionable matters in water to nearby drain/sewer avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5 Landscape and Visual				
5.1 Are retained trees protected by fencing?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.2 Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3 Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Remarks

Follow-up:

- ① Perimeter cut off drains along the southern boundary of the site (170 m) ~~are~~ still not fully constructed. Please provide the residual part.
 - ② Exposed slope surfaces ~~was~~ observed wet. No dusty material was ~~was~~ observed. (closed)
 - ③ Parts of the site have been watered. However, a small part of the site was still dusty. The contractor has watered that part immediately. The contractor was reminded to keep unpaved areas wet.
 - ④ No dusty material was released from the stockpiles (closed).
 - ⑤ No dusty material was released from truck transport (closed).
 - ⑥ Chemical waste storage area has been provided. The contractor was reminded to open the door of the area to keep circulation when chemical waste is stored inside (closed).
 - ⑦ No oil drum (filled) was observed without drip tray (closed).
 - ⑧ All licenses, permits and relevant documents should be kept at the site office (eg. copy of APCO form N4, Discharge license).
 - ⑨ Silty water in the wheel washing facilities should be removed.
 - ⑩ The entrance was not found to be silty (closed).
- Observation:
- ⑫ Dusty material was released during rock breaking operation. The contractor was reminded to water the material ~~before~~.
 - ⑬ Empty oil drums were observed. These drums should be collected and placed properly.



Signatures:

ET Inspector

AMS - Site Rep

Client's Site Agent

Contractor's Representative


Name: Tony Nijp

Name: A. Khan

Name: M. Pi

Date: 12-5-06

Date: 12/5/06

Date: 12-5-06

Appendix 2

Marine Water Quality Monitoring Data

Date	Time	Station	Sample Depth (m)	Water Depth (m)	Sea Temp (°C)	Salinity (ppt)	DO Sat (%age)	DO Conc (mg/ℓ)	Turbidity (NTU)	SS (mg/ℓ)
01-May-06	(mid-ebb)	M1	3.0	5.9	25.2	25.4	93.5	6.7	8	7
01-May-06	(mid-ebb)	M2	3.2	6.4	25.7	23.0	93.7	6.7	7	8
01-May-06	(mid-ebb)	C1	1.5	3.0	25.5	24.9	93.1	6.6	10	10
01-May-06	(mid-ebb)	C2	3.0	6.0	25.3	25.8	94.2	6.7	8	7
01-May-06	(mid-flood)	M1	3.1	6.1	25.2	25.4	92.2	6.6	9	13
01-May-06	(mid-flood)	M2	3.2	6.3	25.1	26.2	91.6	6.5	9	8
01-May-06	(mid-flood)	C1	1.7	3.4	25.3	25.2	90.5	6.4	12	11
01-May-06	(mid-flood)	C2	3.1	6.2	25.2	25.6	91.8	6.6	10	14
05-May-06	(mid-ebb)	M1	3.0	6.0	25.5	25.6	95.6	6.8	6	6
05-May-06	(mid-ebb)	M2	3.0	6.0	25.5	25.5	96.4	6.8	6	7
05-May-06	(mid-ebb)	C1	1.5	3.0	25.6	25.6	97.0	6.9	6	8
05-May-06	(mid-ebb)	C2	3.0	6.0	25.5	25.0	96.0	6.8	4	6
05-May-06	(mid-flood)	M1	3.0	6.0	25.3	25.6	96.5	6.8	6	6
05-May-06	(mid-flood)	M2	3.0	6.0	25.2	25.7	96.1	6.8	4	7
05-May-06	(mid-flood)	C1	1.5	3.0	25.3	25.4	98.3	7.0	6	6
05-May-06	(mid-flood)	C2	3.0	6.0	25.1	25.4	96.4	6.8	3	5
09-May-06	(mid-ebb)	M1	2.9	5.8	27.6	17.6	103.7	7.4	3	3
09-May-06	(mid-ebb)	M2	2.8	5.5	27.8	16.7	112.4	8.1	2	5
09-May-06	(mid-ebb)	C1	1.4	2.8	27.6	17.7	95.0	6.8	2	3
09-May-06	(mid-ebb)	C2	3.0	6.0	26.7	22.3	119.2	8.4	2	4
09-May-06	(mid-flood)	M1	2.8	5.6	27.6	17.7	101.6	7.3	2	3

Date	Time	Station	Sample Depth (m)	Water Depth (m)	Sea Temp (°C)	Salinity (ppt)	DO Sat (%age)	DO Conc (mg/ℓ)	Turbidity (NTU)	SS (mg/ℓ)
09-May-06	(mid-flood)	M2	2.9	5.8	27.7	17.0	112.2	8.0	2	5
09-May-06	(mid-flood)	C1	1.6	3.1	27.5	17.8	94.7	6.8	2	3
09-May-06	(mid-flood)	C2	2.9	5.8	26.7	22.2	118.2	8.4	2	4
12-May-06	(mid-ebb)	M1	2.9	5.8	26.7	24.8	94.3	6.6	5	5
12-May-06	(mid-ebb)	M2	3.0	6.0	26.1	26.7	94.5	6.6	7	4
12-May-06	(mid-ebb)	C1	1.4	2.8	27.1	22.0	93.9	6.6	5	4
12-May-06	(mid-ebb)	C2	3.1	6.2	26.3	25.1	93.1	6.5	5	7
12-May-06	(mid-flood)	M1	3.0	6.0	26.4	25.4	95.7	6.7	4	4
12-May-06	(mid-flood)	M2	3.1	6.1	26.4	24.4	94.8	6.6	3	7
12-May-06	(mid-flood)	C1	1.6	3.1	26.9	22.4	94.5	6.6	4	6
12-May-06	(mid-flood)	C2	3.1	6.2	26.5	24.4	95.4	6.7	4	5
15-May-06	(mid-ebb)	M1	3.1	6.2	25.8	26.6	86.1	6.0	3	3
15-May-06	(mid-ebb)	M2	2.9	5.8	25.8	26.4	86.5	6.1	4	3
15-May-06	(mid-ebb)	C1	1.6	3.1	25.8	26.3	85.5	6.0	3	4
15-May-06	(mid-ebb)	C2	3.0	6.0	25.7	27.0	86.5	6.1	4	4
15-May-06	(mid-flood)	M1	3.0	5.9	25.6	27.2	84.9	5.9	6	6
15-May-06	(mid-flood)	M2	3.1	6.2	25.6	26.2	84.7	5.9	4	4
15-May-06	(mid-flood)	C1	1.7	3.4	25.6	25.6	84.3	6.0	1	4
15-May-06	(mid-flood)	C2	3.2	6.4	25.6	28.0	85.1	5.9	5	3
19-May-06	(mid-ebb)	M1	2.9	5.8	25.8	27.6	101.9	7.1	3	3
19-May-06	(mid-ebb)	M2	3.1	6.1	25.5	27.6	101.3	7.1	3	5

Date	Time	Station	Sample Depth (m)	Water Depth (m)	Sea Temp (°C)	Salinity (ppt)	DO Sat (%age)	DO Conc (mg/ℓ)	Turbidity (NTU)	SS (mg/ℓ)
19-May-06	(mid-ebb)	C1	1.4	2.8	25.8	27.3	102.8	7.1	4	3
19-May-06	(mid-ebb)	C2	3.0	6.0	25.7	27.6	102.2	7.1	3	4
19-May-06	(mid-flood)	M1	3.0	5.9	25.5	27.8	99.8	7.0	4	3
19-May-06	(mid-flood)	M2	3.1	6.1	25.2	27.8	99.1	6.9	3	3
19-May-06	(mid-flood)	C1	1.5	3.0	25.4	27.2	99.7	7.0	5	2
19-May-06	(mid-flood)	C2	3.2	6.3	25.4	27.8	99.2	6.9	4	3
22-May-06	(mid-ebb)	M1	3.0	6.0	25.2	27.5	94.4	6.7	5	5
22-May-06	(mid-ebb)	M2	3.0	6.0	25.3	27.3	93.3	6.6	3	5
22-May-06	(mid-ebb)	C1	1.5	3.0	25.3	27.9	92.8	6.5	6	4
22-May-06	(mid-ebb)	C2	3.0	6.0	25.3	26.0	93.1	6.6	2	5
22-May-06	(mid-flood)	M1	3.0	6.0	25.3	27.7	91.9	6.5	4	5
22-May-06	(mid-flood)	M2	3.0	6.0	25.3	27.4	92.2	6.5	4	3
22-May-06	(mid-flood)	C1	1.5	3.0	25.4	27.2	91.5	6.4	4	4
22-May-06	(mid-flood)	C2	3.0	6.0	25.3	25.8	90.4	6.4	3	6
26-May-06	(mid-ebb)	M1	3.0	6.0	26.6	26.5	96.6	6.8	8	7
26-May-06	(mid-ebb)	M2	3.0	6.0	26.6	23.6	97.1	6.8	7	7
26-May-06	(mid-ebb)	C1	1.5	3.0	26.5	24.2	96.1	6.8	6	6
26-May-06	(mid-ebb)	C2	3.0	6.0	26.5	21.7	97.6	6.8	5	6
26-May-06	(mid-flood)	M1	3.0	6.0	26.7	25.1	100.0	7.0	6	7
26-May-06	(mid-flood)	M2	3.0	6.0	26.7	23.9	97.9	6.9	5	7
26-May-06	(mid-flood)	C1	1.5	3.0	26.7	23.6	99.2	7.0	8	7

Date	Time	Station	Sample Depth (m)	Water Depth (m)	Sea Temp (°C)	Salinity (ppt)	DO Sat (%age)	DO Conc (mg/ℓ)	Turbidity (NTU)	SS (mg/ℓ)
26-May-06	(mid-flood)	C2	3.0	6.0	26.8	22.2	98.5	6.9	6	7
29-May-06	(mid-ebb)	M1	3.0	6.0	26.2	21.4	99.9	7.2	4	5
29-May-06	(mid-ebb)	M2	3.0	6.0	26.0	17.9	99.4	7.3	4	4
29-May-06	(mid-ebb)	C1	1.5	3.0	26.1	14.1	96.7	7.2	7	5
29-May-06	(mid-ebb)	C2	3.0	6.0	26.2	19.5	98.6	7.2	5	5
29-May-06	(mid-flood)	M1	3.0	6.0	25.9	16.8	93.6	6.9	8	7
29-May-06	(mid-flood)	M2	3.0	6.0	25.9	22.2	95.4	6.8	5	5
29-May-06	(mid-flood)	C1	1.5	3.0	25.7	13.6	91.1	6.9	5	6
29-May-06	(mid-flood)	C2	3.0	6.0	26.0	20.2	94.4	6.8	4	5

Notes : “-“ indicates no data is available

Bold indicates Action Level exceedance

Bold indicates Limit Level exceedance

Mean	26.0	24.1	95.9	6.8	4.8	5.4
Maximum	27.8	28.0	119.2	8.4	12.0	14.0
Minimum	25.1	13.6	84.3	5.9	1.3	2.0

Appendix 3

Equipment Calibration Details

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Tubidimeter

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2130B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
0.00 NTU	0.00 NTU
4.00 NTU	4.30 NTU
16.0 NTU	16.7 NTU
80.0 NTU	84.6 NTU
160 NTU	167 NTU
Allowing Deviation	±10%


Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Conductivity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2510B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
1412 uS/cm	1488 uS/cm
6667 uS/cm	6720 uS/cm
58670 uS/cm	59330 uS/cm
Allowing Deviation	±10%



Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Salinity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2520 A and B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
10.0 g/L	10.1 g/L
20.0 g/L	20.3 g/L
30.0 g/L	30.6 g/L
Allowing Deviation	±10%



Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Thermometer

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : In-house Method
Date of Calibration : 23 February,2006

Testing Results :

Reference Temperature (°C)	Recorded Temperature (°C)
18.0 °C	18.2 °C
40.0 °C	40.1 °C
Allowing Deviation	±2.0°C


Alice W.M. Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of DO System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (18th Ed.) 4500-OC & G
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
0.00 mg/L	0.00 mg/L
2.88 mg/L	3.00 mg/L
4.88 mg/L	4.96 mg/L
8.52 mg/L	8.46 mg/L
Allowing Deviation	±0.2 mg/L


Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Turbidimeter

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2130B
Date of Calibration : 04 May,2006

Testing Results :

Expected Reading	Recording Reading
0.00 NTU	0.00 NTU
4.00 NTU	4.30 NTU
16.0 NTU	17.4 NTU
80.0 NTU	83.5 NTU
160 NTU	160 NTU
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Conductivity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2510B
Date of Calibration : 04 May,2006

Testing Results :

Expected Reading	Recording Reading
1412 uS/cm	1387 uS/cm
6667 uS/cm	6781 uS/cm
58670 uS/cm	58910 uS/cm
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch: 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Salinity System

Item: YSI SONDE Environmental Monitoring System
Model No.: 6820-C-M
Serial No.: 00010867
Equipment No.: W-026-27
Calibration Method: This meter was calibrated in accordance with standard method APHA (19th Ed.) 2520 A and B
Date of Calibration: 04 May, 2006

Testing Results:

Expected Reading	Recording Reading
10.0 g/L	10.5 g/L
20.0 g/L	20.9 g/L
30.0 g/L	30.5 g/L
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS



Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Thermometer

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : In-house Method
Date of Calibration : 04 May,2006

Testing Results :

Reference Temperature (°C)	Recorded Temperature (°C)
20.5 °C	20.7 °C
24.5 °C	24.7 °C
Allowing Deviation	±2.0°C

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Tubidimeter

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2130B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
0.00 NTU	0.00 NTU
4.00 NTU	4.30 NTU
16.0 NTU	16.7 NTU
80.0 NTU	84.6 NTU
160 NTU	167 NTU
Allowing Deviation	±10%


Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Conductivity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2510B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
1412 uS/cm	1488 uS/cm
6667 uS/cm	6720 uS/cm
58670 uS/cm	59330 uS/cm
Allowing Deviation	±10%



Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Salinity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2520 A and B
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
10.0 g/L	10.1 g/L
20.0 g/L	20.3 g/L
30.0 g/L	30.6 g/L
Allowing Deviation	±10%



Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Thermometer

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : In-house Method
Date of Calibration : 23 February,2006

Testing Results :

Reference Temperature (°C)	Recorded Temperature (°C)
18.0 °C	18.2 °C
40.0 °C	40.1 °C
Allowing Deviation	±2.0°C


Alice W.M. Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK49674
Sub Batch : 0
Date of Issue: 24/02/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of DO System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 0001093A
Equipment No. : W-026-23
Calibration Method : This meter was calibrated in accordance with standard method APHA (18th Ed.) 4500-OC & G
Date of Calibration : 23 February,2006

Testing Results :

Expected Reading	Recording Reading
0.00 mg/L	0.00 mg/L
2.88 mg/L	3.00 mg/L
4.88 mg/L	4.96 mg/L
8.52 mg/L	8.46 mg/L
Allowing Deviation	±0.2 mg/L


Alice W M Wong
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Turbidimeter

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2130B
Date of Calibration : 04 May,2006

Testing Results :

Expected Reading	Recording Reading
0.00 NTU	0.00 NTU
4.00 NTU	4.30 NTU
16.0 NTU	17.4 NTU
80.0 NTU	83.5 NTU
160 NTU	160 NTU
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Conductivity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2510B
Date of Calibration : 04 May,2006

Testing Results :

Expected Reading	Recording Reading
1412 uS/cm	1387 uS/cm
6667 uS/cm	6781 uS/cm
58670 uS/cm	58910 uS/cm
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Salinity System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2520 A and B
Date of Calibration : 04 May,2006

Testing Results :

Expected Reading	Recording Reading
10.0 g/L	10.5 g/L
20.0 g/L	20.9 g/L
30.0 g/L	30.5 g/L
Allowing Deviation	±10%


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

CERTIFICATE OF ANALYSIS



Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of Thermometer

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : In-house Method
Date of Calibration : 04 May,2006

Testing Results :

Reference Temperature (°C)	Recorded Temperature (°C)
20.5 °C	20.7 °C
24.5 °C	24.7 °C
Allowing Deviation	±2.0°C

CERTIFICATE OF ANALYSIS




Batch: HK51718
Sub Batch : 0
Date of Issue: 17/05/2006
Client: MAUNSELL ENV MGT CNLT LTD
Client Reference:

Calibration of DO System

Item : YSI SONDE Environmental Monitoring System
Model No. : 6820-C-M
Serial No. : 00010867
Equipment No. : W-026-27
Calibration Method : This meter was calibrated in accordance with standard method APHA (18th Ed.) 4500-OC & G
Date of Calibration : 04 May, 2006

Testing Results :

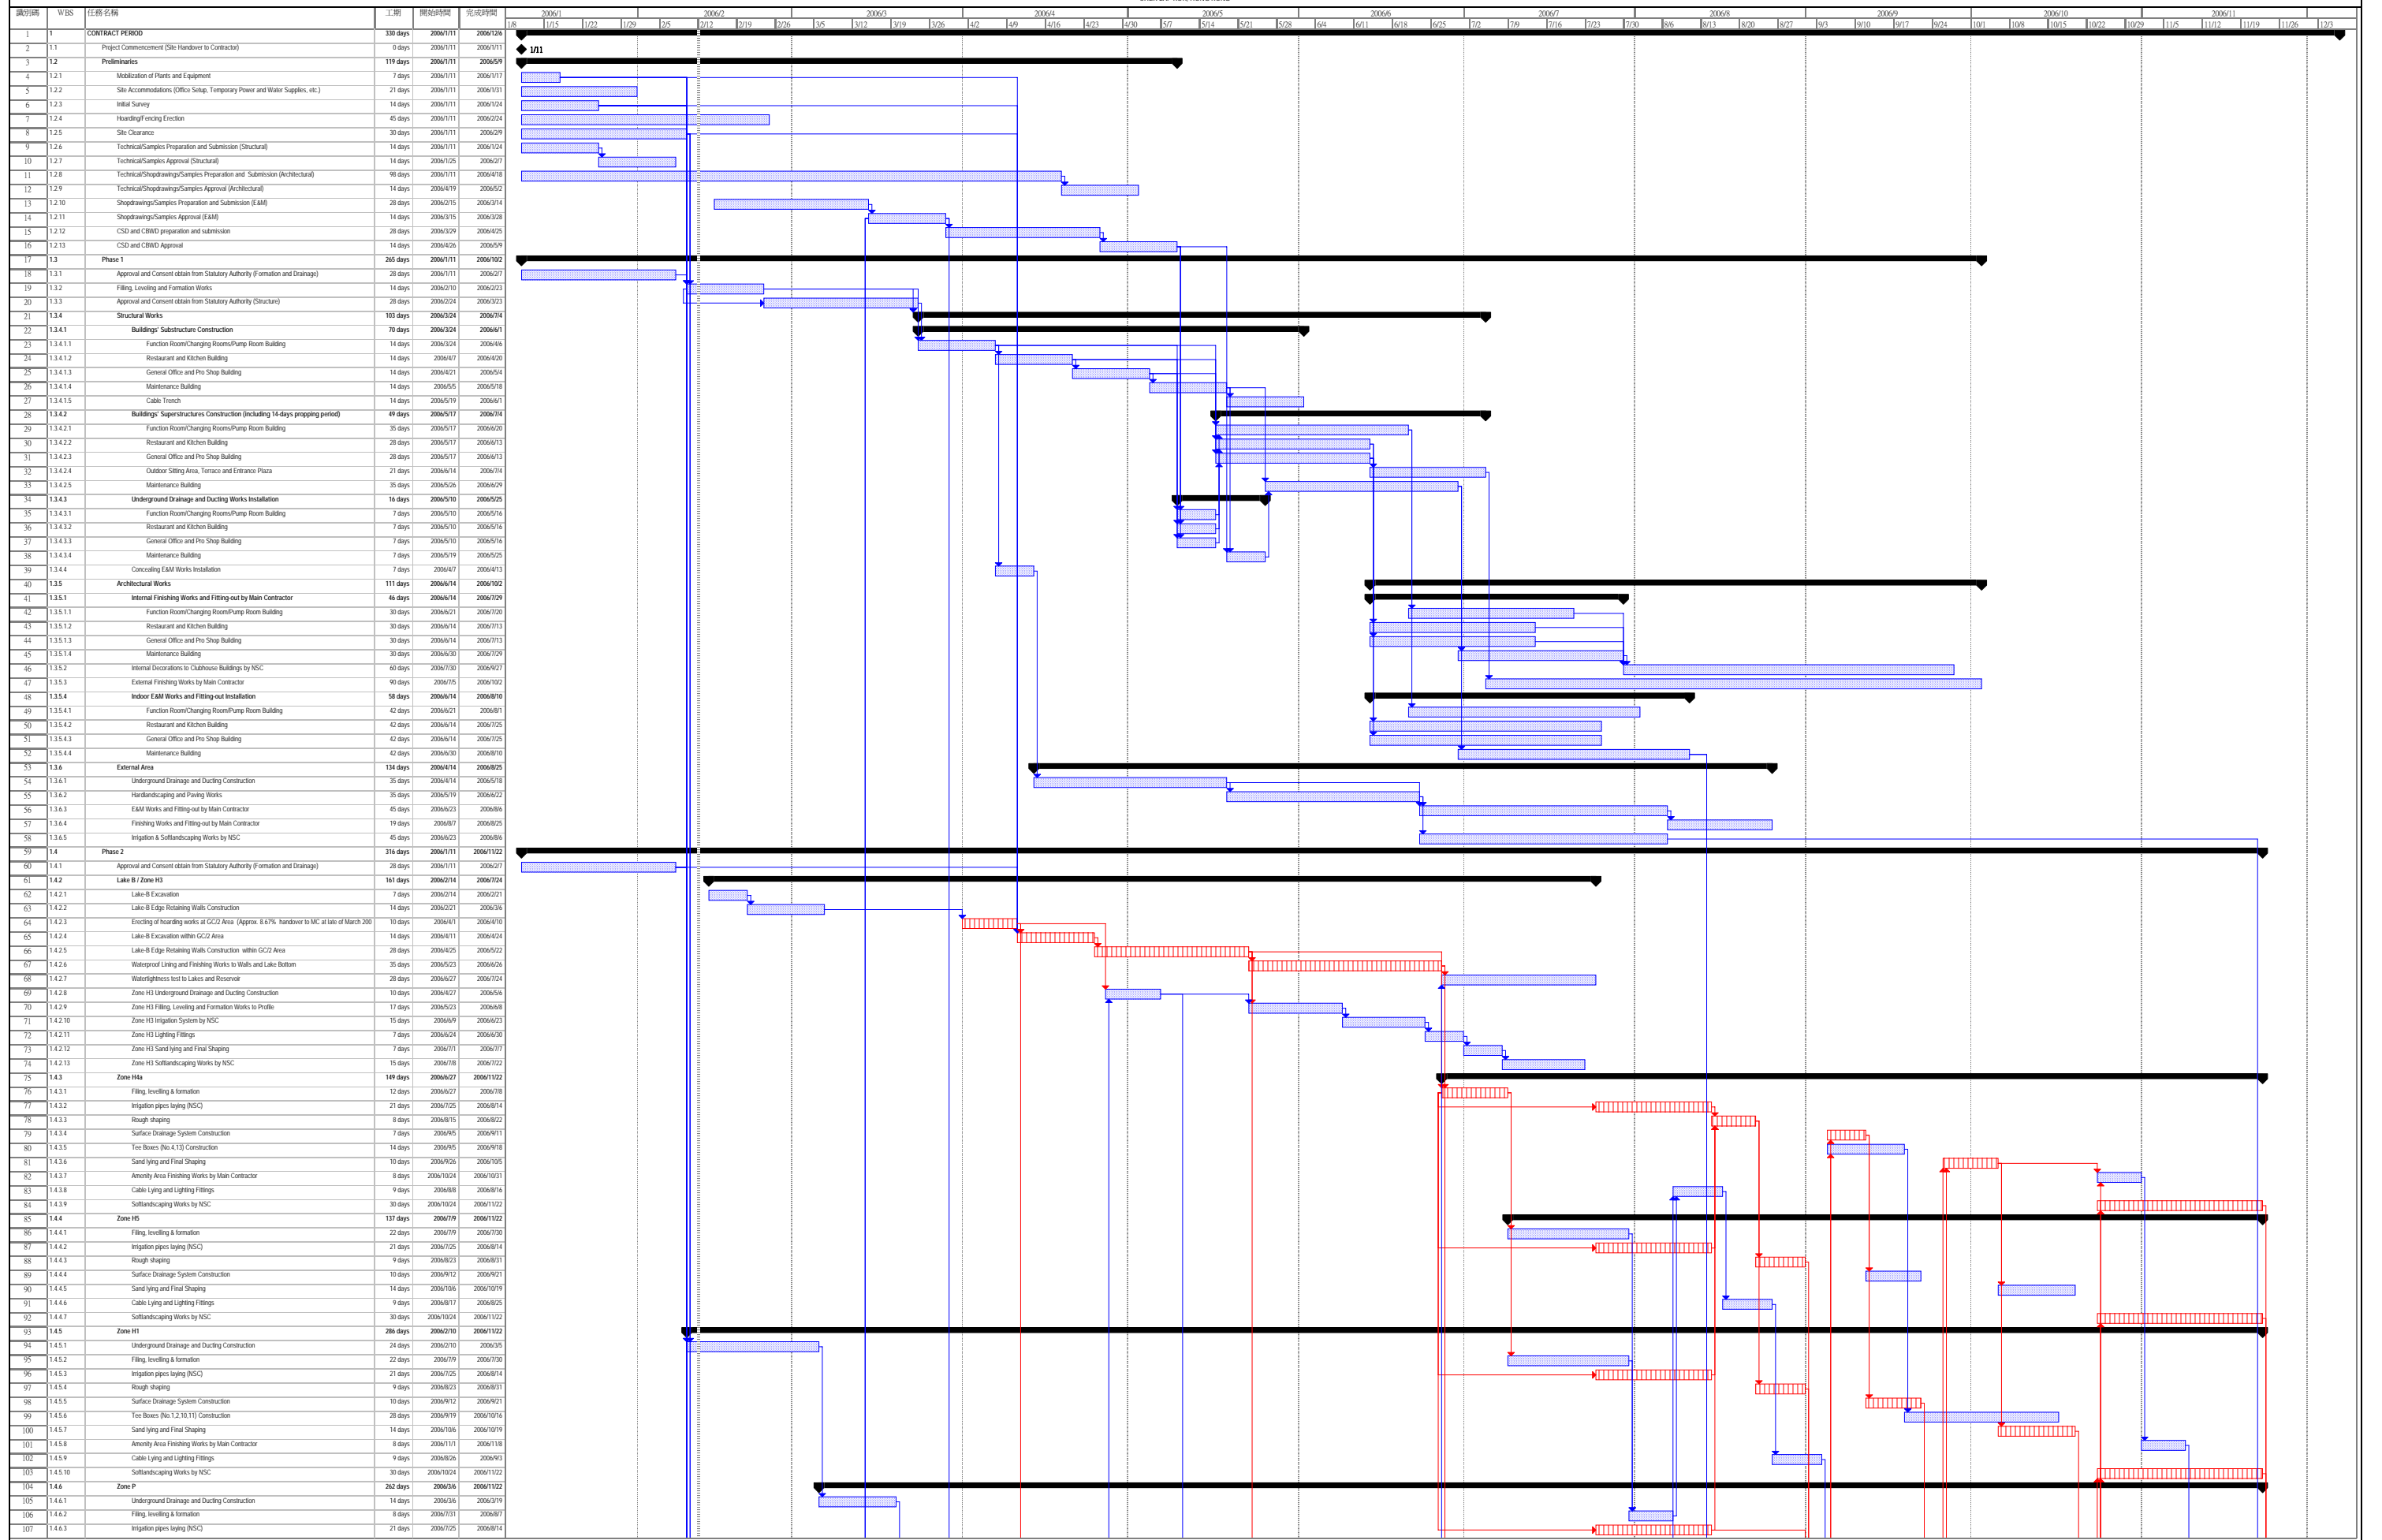
Expected Reading	Recording Reading
0.00 mg/L	0.00 mg/L
4.32 mg/L	4.47 mg/L
6.79 mg/L	6.59 mg/L
8.98 mg/L	8.83 mg/L
Allowing Deviation	±0.2 mg/L


Ms Wong Wai Man, Alice
Laboratory Manager - Hong Kong

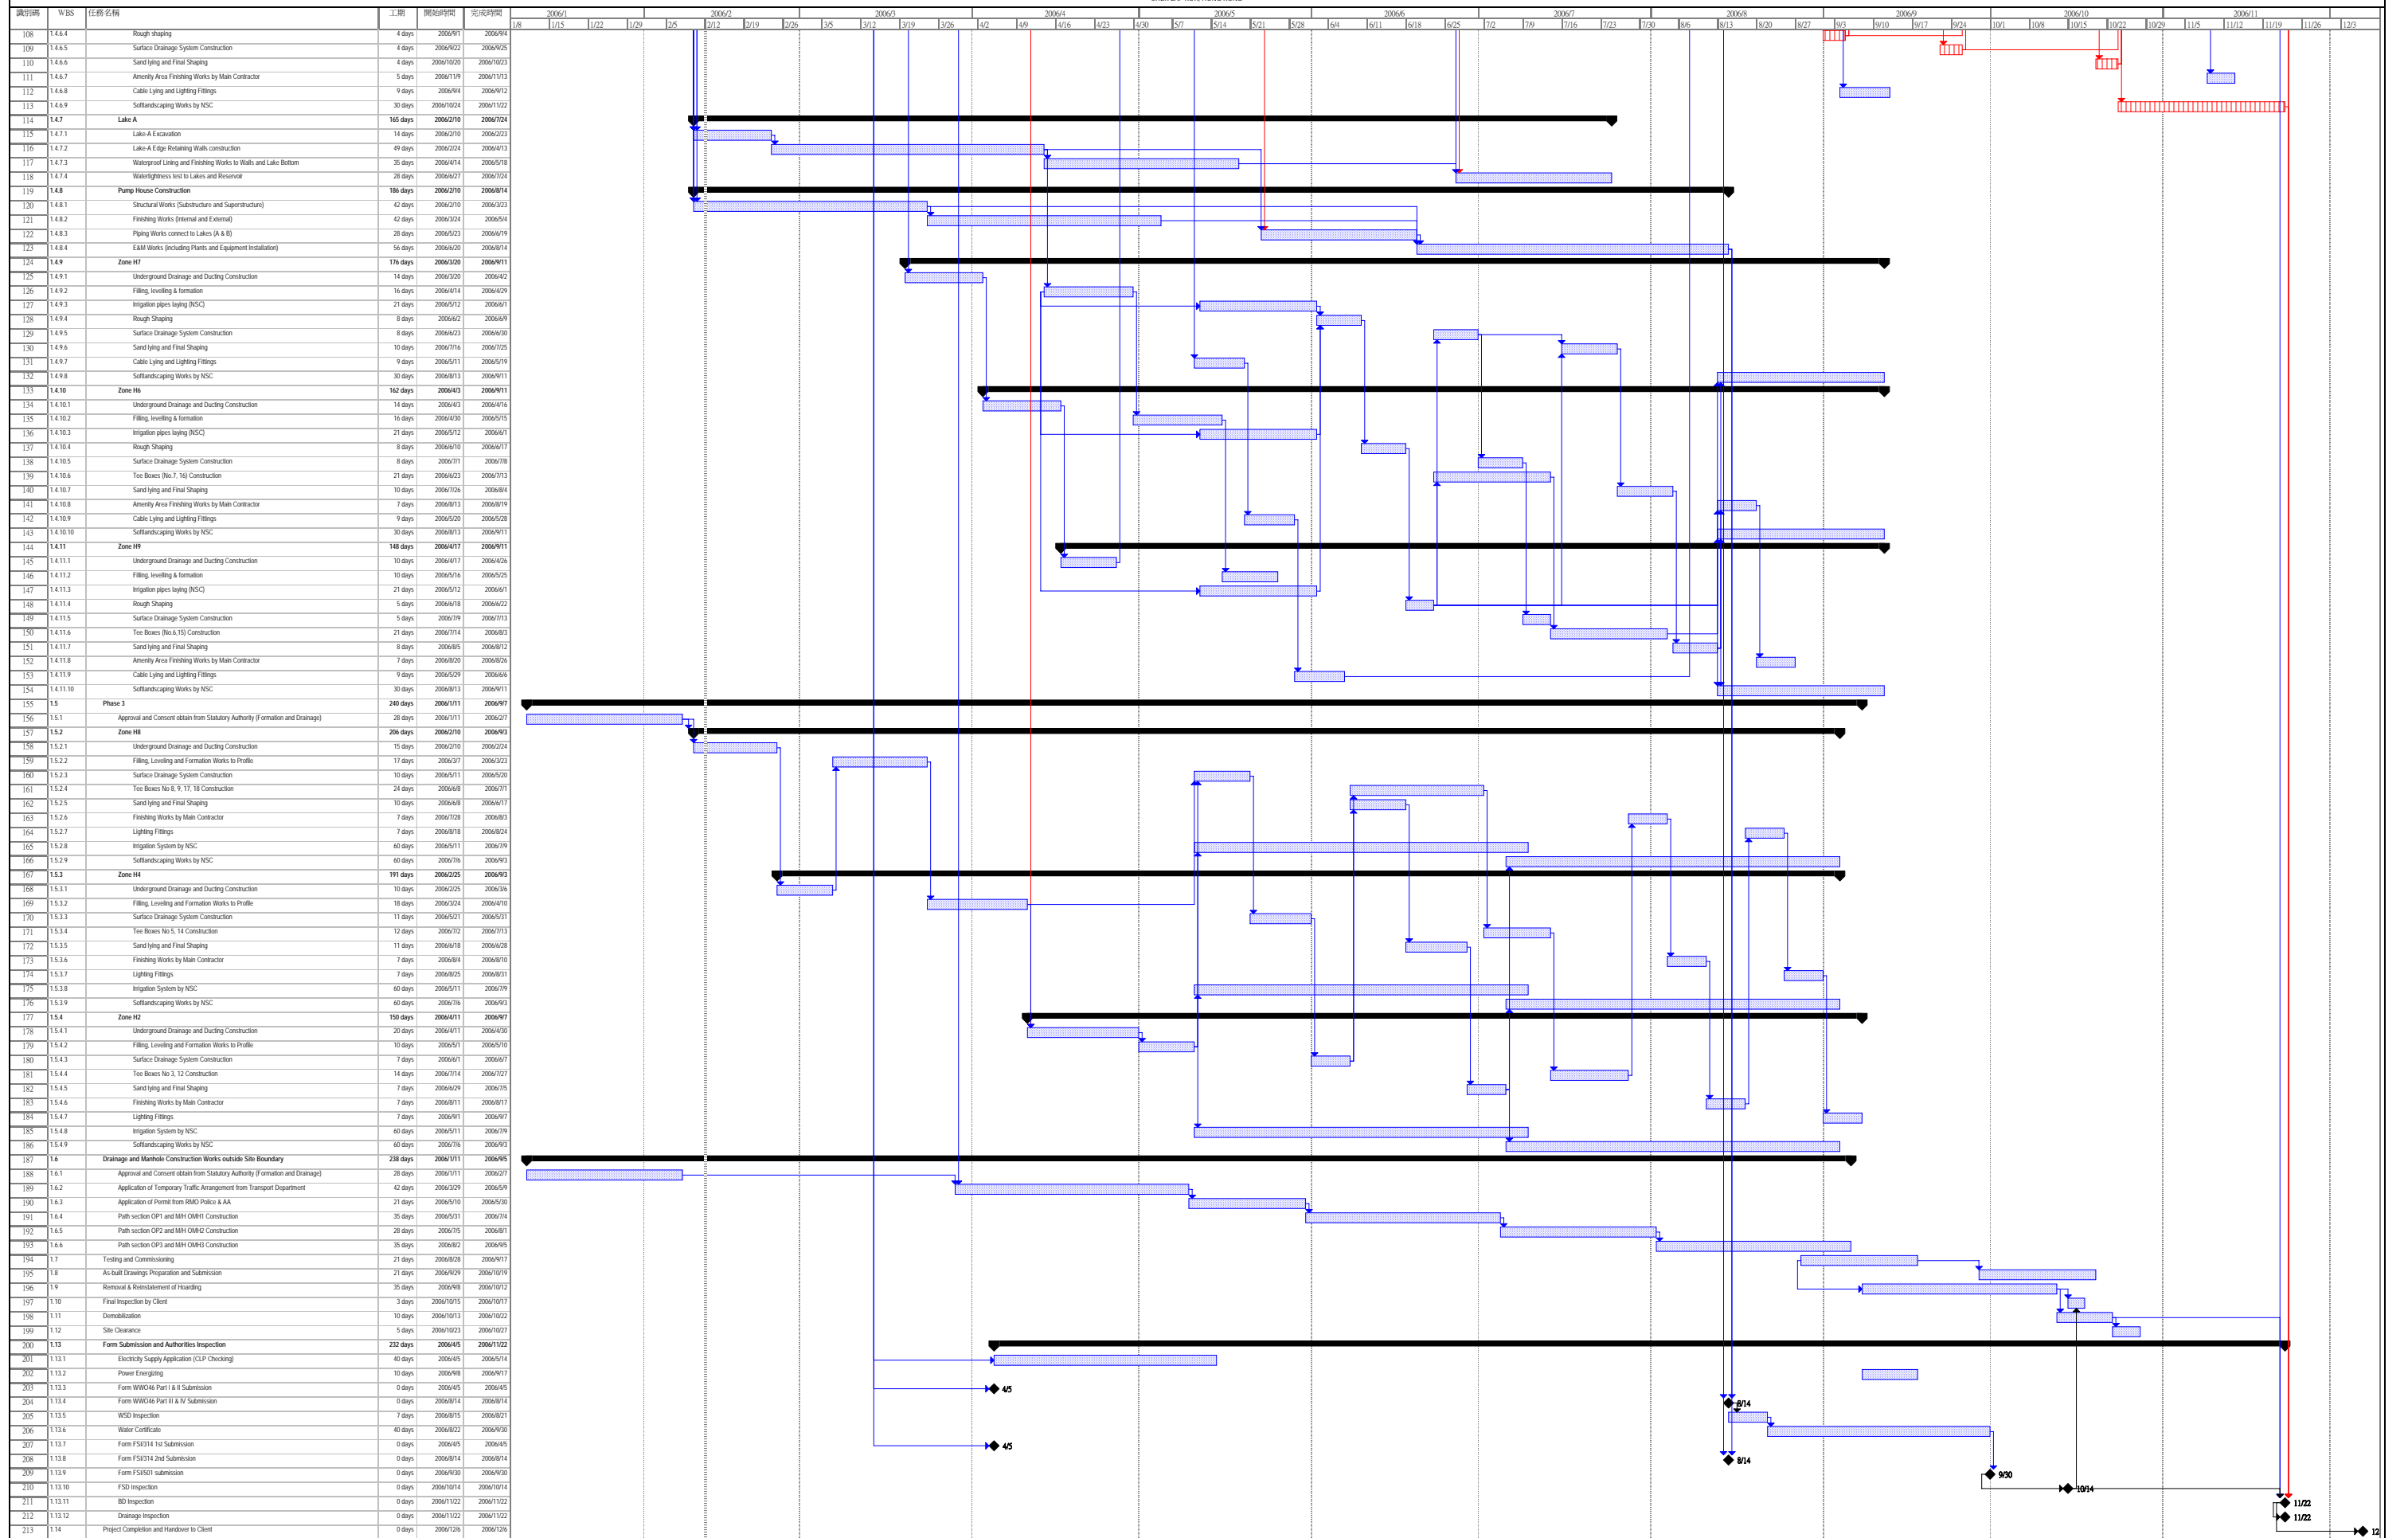
Appendix 4

Works Programme

PROJECT: SKYCIITY GOLF COURSE
LOT NO.825, REP. OF CHEK LAP KOK LOT NO. 1 AND THE EXTENSION THERETO,
CHEK LAP KOK, HONG KONG



PROJECT: SKY CITY GOLF COURSE
LOT NO.825, REP. OF CHEK LAP KOK LOT NO. 1 AND THE EXTENSION THERETO,
CHEK LAP KOK, HONG KONG



Appendix 5

Marine Water Monitoring Schedule for Next Month

**Sky City Golf Course EM&A
Tentative Water Quality Monitoring Schedule for June 2006**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
28-May	29-May	30-May	31-May	01-Jun	02-Jun	03-Jun
	Mid-Flood 07:08 <i>03:52 10:24</i> Mid-Ebb 14:26 <i>10:24 18:28</i>				Mid-Flood 04:50 <i>20:44 12:56</i> Mid-Ebb 17:12 <i>12:56 21:29</i>	
04-Jun	05-Jun	06-Jun	07-Jun	08-Jun	09-Jun	10-Jun
	Mid-Ebb 08:43 <i>06:27 10:59</i> Mid-Flood 13:40 <i>10:59 16:21</i>				Mid-Ebb 11:29 <i>07:46 15:13</i> Mid-Flood 18:23 <i>15:13 21:34</i>	
11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun
	Mid-Flood 06:11 <i>02:59 09:23</i> Mid-Ebb 13:24 <i>09:23 17:26</i>				Mid-Flood 09:12 <i>05:57 12:28</i> Mid-Ebb 16:30 <i>12:28 20:32</i>	
18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun
	Mid-Ebb 07:42 <i>05:14 10:11</i> Mid-Flood 13:05 <i>10:11 15:59</i>				Mid-Ebb 11:21 <i>07:35 15:08</i> Mid-Flood 18:27 <i>15:08 21:46</i>	
25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	01-Jul
		Mid-Flood 06:47 <i>03:27 10:08</i> Mid-Ebb 14:12 <i>10:08 18:16</i>			Mid-Flood 08:47 <i>05:31 12:03</i> Mid-Ebb 16:03 <i>12:03 20:04</i>	
