



Quarterly EM&A Compliance Report

SkyCity Nine Eagles Golf Course

February to April 2014



Project/ Deliverable No.:	7076024 D01/16 Revision No 1
Project Name:	SkyCity Nine Eagles Golf Course
Report Name:	Quarterly EM&A Compliance Report – February to April 2014
Report Date:	May 2014
Report for:	Sky City Nine Eagles Golf Course

PREPARATION, REVIEW AND AUTHORISATION

Revision #	Date	Prepared by	Reviewed by	Approved by
1 (Final)	May 2014	Winnie MA	Antony WONG	Alexi BHANJA

ISSUE REGISTER

Distribution List	Date Issued	Number of Copies
Sky City Nine Eagles Golf Course – Eddie YUNG	May 2014	1 electronic
EPD (EIAO Office) – Kenny LEUNG	May 2014	2 hardcopies + 1 CD-ROM
EPD (Regional Office) – Wilson TAM	May 2014	1 hardcopy
SkyCity Nine Eagles – Vincent LEUNG	May 2014	1 electronic
Asia Turf Solutions – Rick HAMILTON	May 2014	1 electronic
Airport Authority – Sophia LAU	May 2014	1 electronic
SMEC Project File:	May 2014	1 electronic

SMEC COMPANY DETAILS

SMEC Asia Limited

27/F Ford Glory Plaza, 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, Hong Kong T +852 3995 8100 | F +852 3995 8101 smecasia@smec.com | www.smec.com

The information within this document is and shall remain the property of SMEC Asia Limited



CONTENTS

	EXECU	TIVE SU	IMMARY	E-1
1	PROJE	CT DESC	CRIPTION	1-1
	1.1	Overvie	ew	1-1
	1.2	Operati	on	1-1
2	LAKE V	VATER (QUALITY EM&A	2-1
	2.1	EM&A F	Programme	2-1
		2.1.1	Monitoring This Quarter	2-1
		2.1.2	Monitoring Next Quarter	2-1
	2.2	Equipm	ent and Methodology	2-1
	2.3	Mainte	nance and Calibration	2-2
	2.4	Parame	ters Monitored	2-2
	2.5	Monito	ring Locations	2-2
	2.6	Monito	ring Date, Time, Frequency and Duration	2-2
	2.7	Action /	/ Limit Levels	2-3
3	MONI	TORING	RESULTS	3-1
	3.1	Summa	ry of Results	
	3.2	Discuss	ion	
		3.2.1	February 2014	3-1
		3.2.2	March 2014	3-2
		3.2.3	April 2014	3-2
	3.3	Operati	onal Practice	
	3.4	Compla	ints and Notifications of Summons	
4	COMN	1ENTS, F	RECOMMENDATIONS AND CONCLUSIONS	



APPENDICES

- Appendix 1 Equipment Calibration Details
- Appendix 2 Lake Water Quality Monitoring Data
- Appendix 3 Graphical Plots of Monitoring Data for the Past Four Months
- Appendix 4 Aqua Bio-Trol Liquid Product Datasheet

TABLES

- Table 2-1Monitoring Schedule for This Quarter
- Table 2-2 Monitoring Schedule for the Next Quarter
- Table 2-3 In-situ Monitoring Equipment Details
- Table 2-4 Monitoring Frequency
- Table 2-5
 Action and Limit Levels for Lake Water Quality
- Table 2-6E/AP for Lake Water Quality Monitoring
- Table 3-1
 Summary of Compliance Monitoring Data During Reporting Quarter
- Table 3-2 Operational Results

FIGURES

- Figure 1-1 Location of SkyCity Golf Course on the Airport Island
- Figure 1-2 Schematic of Lake Water Control System
- Figure 2-1 Locations for Lake Water Quality Monitoring



EXECUTIVE SUMMARY

The project comprises the construct ion and operation a 9-hole Golf Course at the east side of the North Commercial District (NCD) on the Airport Island as an interim arrangement prior to the area's future development as a business park. The golf facility, known as "SkyCity Nine Eagles Golf Course" serves airport passengers and workers as well as the general public.

According to the approved EM&A Manual, monthly compliance monitoring of lake water quality at four locations (W1 and W2 in Lake A and W3 and W4 in Lake B) is required during the Operation Period, with reporting on a quarterly basis. Parameters monitored comprise Suspended Solids (SS), Dissolved Oxygen (DO), Biochemical Oxygen Demand (BOD₅), nitrogen, phosphorous, temperature and salinity.

This is the twenty-eighth Quarterly Compliance report covering February to April 2014 and complies with the reporting requirements stated in the approved EM&A Manual.

In February 2014, there was no exceedance of any parameter at any location.

In March 2014, there was no exceedance of any parameter at any location.

In April 2014, there was no exceedance of any parameter at any location.

As soon as monthly results were available, EPD and the Golf Course Supervisor were notified of any exceedances, as required by the Event/Action Plan. In January 2014, the Golf Course Supervisor was advised that lake water was of an acceptable quality and that the control valve could be opened if needed. This has remained the situation during February, March and April 2014.

There were no complaints, notifications of summons received during the reporting quarter. There were also no openings of the control valve, emergency or otherwise. As such, there was no off-site release of lake water and therefore no impact to the marine environment.



1 PROJECT DESCRIPTION

1.1 Overview

The project comprises the construct ion and operation a 9-hole Golf Course at the east side of the North Commercial District (NCD) on the Airport Island as an interim arrangement prior to the area's future development as a business park (see *Figure 1-1*). The golf facility, known as "SkyCity Nine Eagles Golf Course" serves airport passengers and workers as well as the general public.

The Project is managed by SkyCity Nine Eagles Golf Course, who has engaged Asia Turf Solutions Ltd to establish and maintain the turfgrass of the Golf Course. SMEC Asia Ltd has been employed as the Environmental Team (ET) for the Operation Period since May 2010 and has engaged ALS Technichem Pty Ltd as the HOKLAS accredited testing laboratory to carry out lake water analysis.

Construction of the golf course was completed on 31 December 2006, the first phase of the Operation Period was completed on 30 April 2007, and the second (and current) phase commenced on 1 May 2007.

1.2 Operation

The Golf Course has been designed to contain water within two artificial lakes, which are linked together by two underwater pipes. The lakes provide a source of freshwater for irrigation. All rainwater and surplus irrigation water collected within the Golf Course will drain back into the lakes for reuse, through a sub-soil drainage system.

The lakes are maintained at a capacity of 15,000m³. This is not "full" but is the level that provides the required visual appearance. During the winter (dry) months, however, the lake water may fall below this level. The maximum capacity of the lakes is 20,000m³.

If the capacity of the lakes exceeds 20,000m³, then the Golf Course may flood. To avoid this, the Golf Course Supervisor can authorise the opening of a control valve to allow the water to overflow from the lakes into storm drains that discharge off-site via Outfall No. 8. However, the valve can only be opened if the lake water monitoring results indicate that water is of an acceptable quality. Under normal circumstances, the control valve remains closed and discharge off-site is not possible. All opening/closing of the control valve is logged on site.

If the latest lake water monitoring results indicate that water is not of an acceptable quality, then the valve cannot be opened, the lake water cannot overflow and the Golf Course may begin to flood. This is part of the mitigation design to prevent off-site discharge of water that does not meet the required standard.

The bund that surrounds the site is at least 1.5m high and up to 90,000m³ of floodwater can be retained within the Golf Course in addition to the 20,000m³ lake capacity. In this situation, water samples from the flooded Golf Course will be taken more frequently. Only when water has returned to an acceptable quality will the control valve be opened to allow water to overflow from the lake and into off-site storm drains that discharge via Outfall No. 8, thereby allowing the flood to recede.

The system by which this water control is achieved is shown in *Figure 1-2*.




Figure 1-1 Location of SkyCity Golf Course on the Airport Island



Source: Image courtesy of Airport Authority

Location Map




Key

- Terminal 2 & SkyPlaza (Retail, F&B & Entertainment) 二號客運大樓及翔天廊(零售、食肆及娛樂區)
- 2 HKIA Tower 機場行政大樓
- AsiaWorld Expo 亞洲國際博覽館
- 4 2nd on-airport hotel 第二間機場酒店
- SkyPier 海天客運碼頭
- 6 SkyCity Nine Eagles Golf Course 航天城高爾夫球場
- Airport World Trade Centre 暫名:機場世界貿易中心



Figure 1-2 Schematic of Lake Water Control System

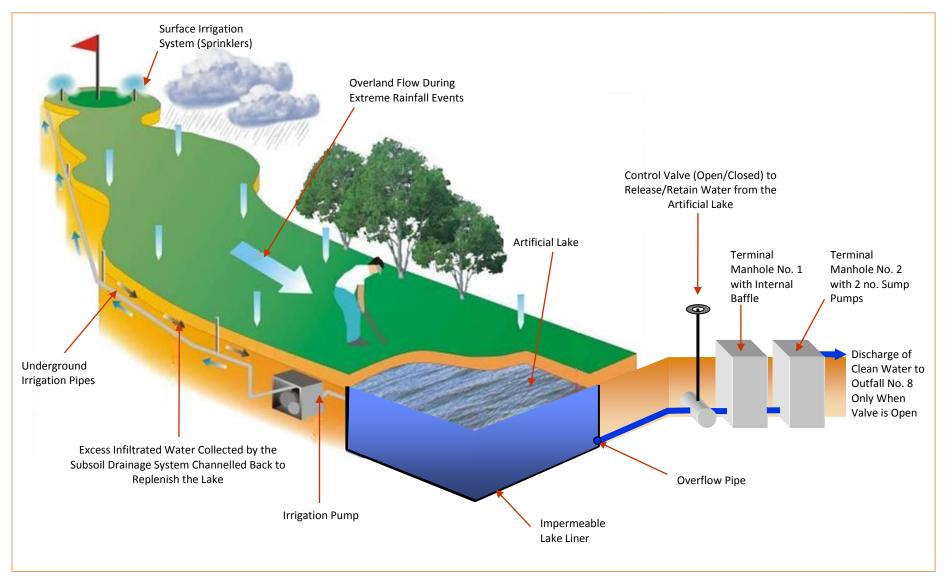



2 LAKE WATER QUALITY EM&A

2.1 EM&A Programme

Monitoring of Dissolved Oxygen (DO) in mg/ ℓ , Suspended Solids (SS) in mg/ ℓ , Biochemical Oxygen Demand (BOD₅) in mg/ ℓ , Total Nitrogen in mg/ ℓ , Total Phosphorous in mg/ ℓ , Salinity in g/ ℓ , and temperature in °C was carried out by the ET to ensure that any deterioration in lake water quality could be readily detected and timely action could be taken to rectify the situation if this was due to site operations.

DO, temperature and salinity were measured in-situ whilst other parameters were determined in a HOKLAS-accredited laboratory.

2.1.1 Monitoring This Quarter

The actual lake water monitoring schedule for this quarter (February to April 2014) is given in *Table 2-1*, below.

Sampling Date	Sampling Locations
14 February 2014	W1 to W4
14 March 2014	W1 to W4
10 April 2014	W1 to W4

Table 2-1 Monitoring Schedule for This Quarter

2.1.2 Monitoring Next Quarter

The planned lake water monitoring schedule for the next quarter (May to July 2014) is given in *Table 2-2*, below.

Table 2-2 Monitoring Schedule for the Next Quarter

Sampling Date	Sampling Locations
9 May 2014	W1 to W4
13 Jun 2014	W1 to W4
11 July 2014	W1 to W4

2.2 Equipment and Methodology

Because of the relatively shallow water, in-situ measurements and water sampling were conducted at 0.5m from the surface (the mid-point of the 1m deep lake). Water samples for all monitoring parameters were collected, stored, preserved and analysed according to APHA Standard Methods for the Examination of Water and Wastewater, 19th Ed, #17.

In-situ monitoring was carried out using a DO concentration and DO saturation were carried out using a YSI Model 85 CE-C-M-Y multi-parameter meter and the range, resolution and accuracy of the equipment is provided in *Table 2-3*.



Table 2-3 In-situ Monitoring Equipment Details

In-situ Parameters	Measuring Devices	Measurement Precision	
Dissolved Oxygen		0.1mg/ℓ and 0.1%	
Salinity	YSI Professional Plus	0.1ppt (or g/ℓ)	
Temperature		0.1°C	

A Kahlisco water sampler was used to obtain water samples for subsequent SS analysis in the laboratory. A sufficient volume of the sample is collected in clean, high density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to the ALS laboratory immediately after monitoring. The analysis of the collected samples starts by the next working day following APHA *Standard Methods* #2540D.

2.3 Maintenance and Calibration

All in-situ monitoring instruments are calibrated and certified by ALS at monthly intervals throughout all stages of the lake water quality monitoring programme.

The YSI Multi-purpose Meter is calibrated once per monitoring day by the wet bulb method. Calibration at the ALS laboratory is carried out once every month in a water sample of known dissolved oxygen concentration. The sensor is immersed in the water and after thermal equilibration, the known mg/ ℓ value is keyed in and the calibration is carried out automatically. Calibration details are provided in *Appendix 1*.

2.4 Parameters Monitored

The following parameters are monitored and compared to Action/Limit (A/L) Levels:

- Dissolved Oxygen
- Suspended Solids
- BOD₅
- Total Nitrogen
- Total Phosphorous

There are no A/L Levels for temperature or salinity – these parameters are recorded for information only.

2.5 Monitoring Locations

Monitoring locations together with grid references are shown in *Figure 2-1*. Monitoring Stations are designated as W1, W2, W3 and W4.

2.6 Monitoring Date, Time, Frequency and Duration

In accordance with the EM&A Manual, the monitoring frequency of lake water quality is shown as *Table 2-4*.



Table 2-4 Monitoring Frequency

	Operation Phase				
	Below A/L Level A/L Level Exceedance				
Monitoring Frequency	Monthly	Weekly			

2.7 Action / Limit Levels

According to the approved EM&A manual, the A/L Levels for the compliance monitoring (for monitoring locations W1 to W4) are shown in *Table 2-5*, below.

Table 2-5 Ac	tion and Limit I	evels for Lake	Water Quality
--------------	------------------	----------------	---------------

Devementer	Acceptable Standard (mg/&)			
Parameter	Action Level	Limit Level		
Suspended Solids	20	30		
BOD ₅	13.5	20		
Dissolved Oxygen	4	3		
Total Nitrogen	20	30		
Total Phosphorous	3.5	5		

In case of exceedance of A/L Levels caused by the operation of the Golf Course, the ET shall immediately implement the Event/ Action Plan (E/AP), shown in *Table 2-6*, below, in order to resolve lake water quality problems:

Table 2-6 Event/Action P for Lake Water Quality Monitoring

Event	Action
Exceedance of Action Level	• Notify the Golf Course Supervisor of the exceedance, providing full details (time, location, parameter, level, etc.)
	 Increase the frequency of monitoring of the particular parameter(s) to "Action/Limit Level Exceedance" as shown in <i>Table 2-4</i>
	 If water quality continues to worsen, it may be prudent to review the Turfgrass Management Plan (TMP) in terms of application of nutrients and agree any revisions with the Golf Facility Supervisor
	 Notify the Golf Facility Supervisor when water quality falls below "Action Level" and reduce monitoring frequency to "Below Action/Limit Level" as shown in <i>Table 2-4</i>
Exceedance of Limit Level	 Notify EPD and Golf Course Supervisor of the exceedance, providing full details (time, location, parameter, level, etc.)
	Suspend any ongoing application of organic nutrients
	 Determine the likely cause of the exceedance(s) Review the TMP in terms of application of nutrients and agree any revisions with the Golf Facility Supervisor Continue to irrigate the Golf Course using lake water
	• Increase the frequency of monitoring of the particular parameter(s) to "Action/Limit Level Exceedance" as shown in <i>Table 2-4</i> (if not already at this frequency) to demonstrate the effectiveness of remedial measures and to confirm that water quality has returned to acceptable levels
	 Notify EPD and Golf Course Supervisor when water quality falls below "Action Level" (not "Limit Level") and reduce monitoring frequency to "Below Action/Limit Level" as shown in <i>Table 2-4</i>



Figure 2-1 Locations for Lake Water Quality Monitoring







- Overflow from Lake into Control Valve
- Underground Pipe for Clean Flow
- Connection to Outfall No. 8
- Underground Pipes Connecting Lakes A and B



3 MONITORING RESULTS

3.1 Summary of Results

A summary of scheduled lake water monitoring results for the reporting quarter is provided in *Table 3-1*, below. Detailed results are provided in *Appendix 2* and graphical plots since commencement of the second phase of Operation are given in *Appendix 3*.

Monitoring Location		Salinity (g/ e)	Temperature (^o C)	SS (mg/8)	BOD ₅ (mg/8)	DO Saturation (%age)	DO Concentration (mg/8)	Total Nitrogen (mg/ ĉ)	Total Phosphorous (mg/e)
	Mean	0.1	18.0	10	2.3	97.1	9.9	1.0	0.0
W1	Minimum	0.1	12.8	5	2.0	88.2	8.2	0.6	0.0
	Maximum	0.1	22.4	19	3.0	102.0	10.8	1.4	0.1
	Mean	0.1	17.8	9	2.3	98.3	10.0	0.9	0.0
W2	Minimum	0.1	11.7	5	2.0	87.0	8.1	0.6	0.0
	Maximum	0.1	22.4	18	3.0	106.0	10.9	1.3	0.1
	Mean	0.1	17.0	10	3.3	97.3	10.0	1.0	0.1
W3	Minimum	0.1	9.7	4	2.0	88.8	8.2	0.8	0.0
	Maximum	0.1	22.4	20	5.0	102.0	11.0	1.2	0.1
	Mean	0.1	17.1	11	3.0	97.4	9.8	1.0	0.1
W4	Minimum	0.1	10.0	6	2.0	88.3	8.1	0.8	0.0
	Maximum	0.1	22.5	19	4.0	102.0	10.7	1.1	0.1

 Table 3-1
 Summary of Compliance Monitoring Data during Reporting Quarter

Note: Bold indicates Action Level exceedance; Bold indicates Limit Level exceedance.

3.2 Discussion

3.2.1 February 2014

In February 2014, there was no exceedance of any parameter at any location. The continued reduction in SS concentrations was brought about, in part, by the continuing cold weather, which slowed algal growth significantly. Therefore, in accordance with the EM&A Manual, the Golf Facility Supervisor was advised that lake water was considered to be of an acceptable quality for discharge into the surrounding marine waters and that **the control valve can be opened if needed to allow discharge off-site.**

Since there were no exceedances recorded, the Event/Action Plan specified in the EM&A Manual did not need to be implemented this month.



3.2.2 March 2014

In March 2014, there was no exceedance of any parameter at any location. The continued reduction in SS concentrations was brought about, in part, by the continuing cold weather, which slowed algal growth significantly. Therefore, in accordance with the EM&A Manual, the Golf Facility Supervisor was advised that lake water was considered to be of an acceptable quality for discharge into the surrounding marine waters and that **the control valve can be opened if needed to allow discharge off-site.**

Since there were no exceedances recorded, the Event/Action Plan specified in the EM&A Manual did not need to be implemented this month.

3.2.3 April 2014

In April 2014, there was no exceedance of any parameter at any location, however, SS concentrations at all monitoring locations increased compared to the previous month. This was likely due to the rising temperatures in April increasing algal growth. The DO levels were appreciably lower than last month because the fountains in both lakes were not operating to aerate the water. In accordance with the EM&A Manual, the Golf Facility Supervisor was advised that lake water was considered to be of an acceptable quality for discharge into the surrounding marine waters and that **the control valve can be opened if needed to allow discharge off-site.**

Since there were no exceedances recorded, the Event/Action Plan specified in the EM&A Manual did not need to be implemented this month.

3.3 Operational Practice

Table 3-2, below, shows the operational practice during the reporting quarter, i.e., the activities relating to the management of water in the lakes.

During the reporting quarter, the control valve could be opened if needed because lake water quality was of an acceptable quality for discharge. However, there was no need to open the control valve and so no water was actually discharged off-site.

Month	Month-end Lake Water Depth (m)	Can Control Valve Be Opened?	Was Control Valve Opened?	Quantity of Water Discharged (m ³)
February 2014	0.7	Yes	No	0
March 2014	0.9	Yes	No	0
April 2014	1.2	Yes	No	0

Table 3-2 Operational Results

3.4 Complaints and Notifications of Summons

During the reporting quarter, there were no complaint received and no notifications of summons. There were also no openings of the control valve, emergency or otherwise.



4 COMMENTS, RECOMMENDATIONS AND CONCLUSIONS

This is the twenty-eighth Quarterly Compliance report covering EM&A from February to April 2014 and complies with the reporting requirements stated in the approved EM&A Manual.

Compliance monitoring of lake water quality is required on a monthly basis, with an increase in frequency to weekly if there are Action or Limit Levels exceedances caused by the operation of the Golf Course. Parameters monitored comprise Suspended Solids (SS), Dissolved Oxygen (DO), Biochemical Oxygen Demand (BOD₅), nitrogen, phosphorous, temperature and salinity.

In February 2014, there was no exceedance of any parameter at any location.

In March 2014, there was no exceedance of any parameter at any location.

In April 2014, there was no exceedance of any parameter at any location.

As soon as monthly results were available, EPD and the Golf Course Supervisor were notified of any exceedances, as required by the Event/Action Plan. In January 2014, the Golf Course Supervisor was advised that lake water was of an acceptable quality and that the control valve could be opened if needed. This has remained the situation during February, March and April 2014.

Based on observation, gradual cooling of lake the water over the winter slowed down algal growth in both lakes, which significantly reduced the SS concentrations at all monitoring locations during the reporting quarter. However, as temperatures began to rise in April, SS concentrations also began to increase as a result of renewed algal growth due to the warmer water. It is expected that there will be exceedances in SS concentrations in the months ahead due to greater algal growth resulting from the steadily increasing water temperatures. Bio-Trol will continue to be applied each month to control the expected algal growth.

There were no complaints, notifications of summons received during the reporting quarter. There were also no openings of the control valve, emergency or otherwise. As such, there was no off-site release of lake water and therefore no impact to the marine environment.



APPENDIX 1

Equipment Calibration Details



ALS Technichem (HK) Pty Ltd 11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street Kwai Chung, N.T., Hong Kong T: +852 2610 1044 F: +852 2610 2021 www.alsglobal.com

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR ALEXI BHANJA CLIENT: SMEC ASIA LIMITED ADDRESS: 27/F, FORD GLORY PLAZA, 37-39 WING HONG STREET, CHEUNG SHA WAN, KOWLOON, HONG KONG. PROJECT: SKY CITY GOLF COURSE

WORK ORDER:	HK1334799
SUB-BATCH:	1
LABORATORY:	HONG KONG
DATE RECEIVED:	
DATE OF ISSUE:	07/01/2014

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory. Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Dissolved Oxygen and Temperature
Multimeter
YSI
YSI Professional Plus
09K100735
13 December, 2013

NOTES

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee, Richard

Mr. Fung Lim Chee, Richard General Manager -Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order:	HK1334799	
SUB-BATCH:	1	
Date of Issue:	07/01/2014	
Client:	SMEC ASIA LIMITED	



Description: Brand Name: Model No.: Serial No.:	Multimeter YSI YSI Professional Plus 09K100735		
Equipment No.: Date of Calibration:	 13 December, 2013	Date of next Calibration:	13 March, 2014

Parameters:

Dissolved Oxygen Method Ref: APHA (21st edition), 45000: G

istical (difficient), isocord				
Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)		
3.11	3.30	0.19		
5.16	5.36	0.20		
8.82	8.82	0.00		
	Tolerance Limit (±mg/L)	0.20		

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	l Reading (°C) Displayed Reading (°C)	
9.0	8.4	-0.6
20.0	20.0 19.6	
38.0	38.3	0.3
	Tolerance Limit (±°C)	2.0

Mr. Fung Lim Chée, Richard General Manager Greater China & Hong Kong



ALS Technichem (HK) Pty Ltd 11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street Kwai Chung, N.T., Hong Kong T: +852 2610 1044 F: +852 2610 2021 www.alsglobal.com

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR ALEXI BHANJA CLIENT: SMEC ASIA LIMITED ADDRESS: 27/F, FORD GLORY PLAZA, 37-39 WING HONG STREET, CHEUNG SHA WAN, KOWLOON, HONG KONG. PROJECT: SKY CITY GOLF COURSE

HK1411183
1
HONG KONG
17/04/2014

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory. Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Scope of Test:	Dissolved Oxygen and Temperature
Description:	YSI Multimeter
Brand Name:	YSI
Model No.:	YSI PRO 20
Serial No.:	12C100570
Equipment No.:	
Date of Calibration:	15 January, 2014

NOTES

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee, Richard General Manager -Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order:		
SUB-BATCH:		
Date of Issue:		
Client:		

HK1411183 1 17/04/2014 SMEC ASIA LIMITED



Description:	YSI Multimeter		
Brand Name:	YSI		
Model No.:	YSI PRO 20		
Serial No.:	12C100570		
Equipment No.:			
Date of Calibration:	15 January, 2014	Date of next Calibration:	15 April, 2014

Parameters:

Dissolved Oxygen	Method Ref: APHA (21st edition), 45000: G				
	Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)		
	3.26	3.32	+0.06		
	6.64	6.74	+0.10		
	9.17	9.03	-0.14		
		Tolerance Limit (±mg/L)	0.20		

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)		
8.5	8.3	-0.2		
22.0 42.0	22.0 42.8	0.0 +0.8		
	Tolerance Limit (±°C)	2.0		

Mr. Fung Lim Chee, Richard General Manager -Greater China & Hong Kong



APPENDIX 2

Lake Water Quality Monitoring Data



Date	Time	Station	Salinity (g/&)	Temperature (°C)	SS (mg/&)	BOD5 (mg/ℓ)	DO Sat (%Saturation)	DO Conc (mg/ℓ)	Total Nitrogen (mg/ℓ)	Total Phosphorous (mg/€)
	7:15	W1	0.1	16.5	7	2	101.0	10.1	1.2	0.0
14-February-14	7:16	W2	0.1	16.1	6	2	102.0	10.3	1.2	0.0
	7:40	W3	0.1	15.1	18	4	102.0	10.5	1.2	0.1
	7:31	W4	0.1	15.1	19	3	102.0	10.4	1.2	0.1
	7:15	W1	0.1	12.8	5	2	101.0	10.8	1.4	0.0
14-March-14	7:20	W2	0.1	11.7	5	2	102.0	10.9	1.3	0.0
	7:30	W3	0.1	9.7	4	3	102.0	11.0	1.2	0.0
	7:35	W4	0.1	10.0	6	3	102.0	10.6	1.1	0.0
	7:10	W1	0.1	18.8	7	2	102.0	10.6	0.6	0.0
	7:15	W2	0.1	19.2	5	2	106.0	10.9	0.6	0.0
11-April-14	7:40	W3	0.1	18.8	6	2	101.0	10.9	0.8	0.0
	7:31	W4	0.1	18.9	7	2	102.0	10.7	0.8	0.0
		·				·	·			
		Mean	0.1	17.5	10	3	97.5	9.9	1.0	0.0
		Minimum	0.1	9.7	4	2	87.0	8.1	0.6	0.0
	I	Maximum	0.1	22.5	20	5	106.0	11.0	1.4	0.1


Note: Bold indicates Action Level exceedance; Bold indicates Limit Level exceedance




APPENDIX 3


Graphical Plots of Monitoring Data for the Past Four Months




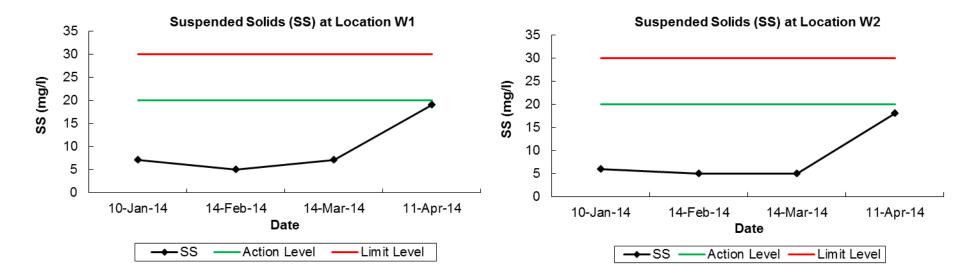

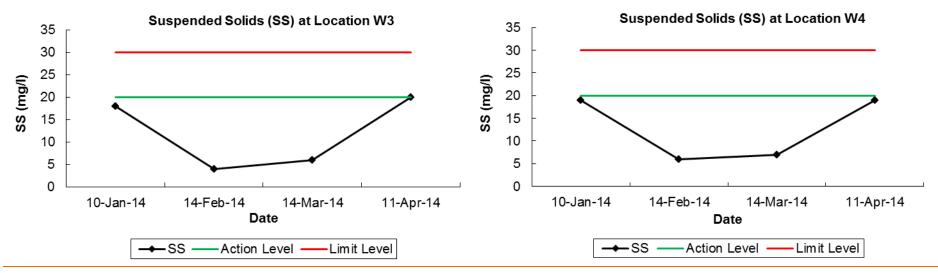





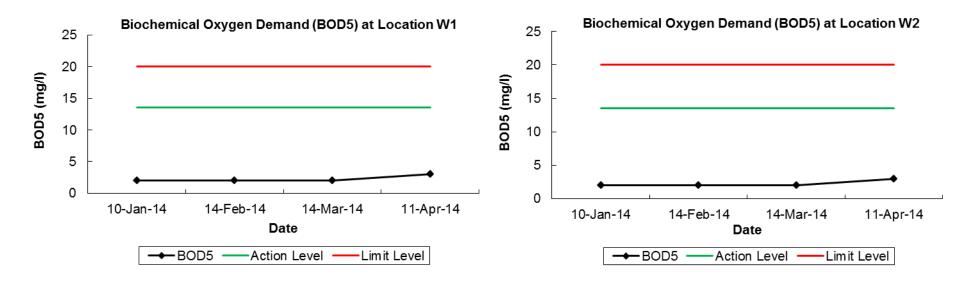


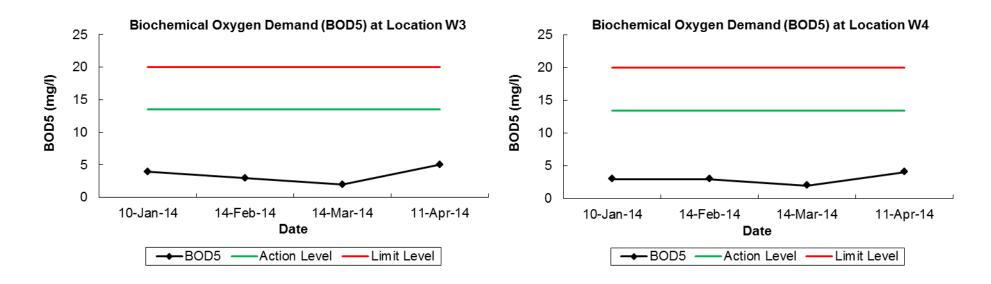



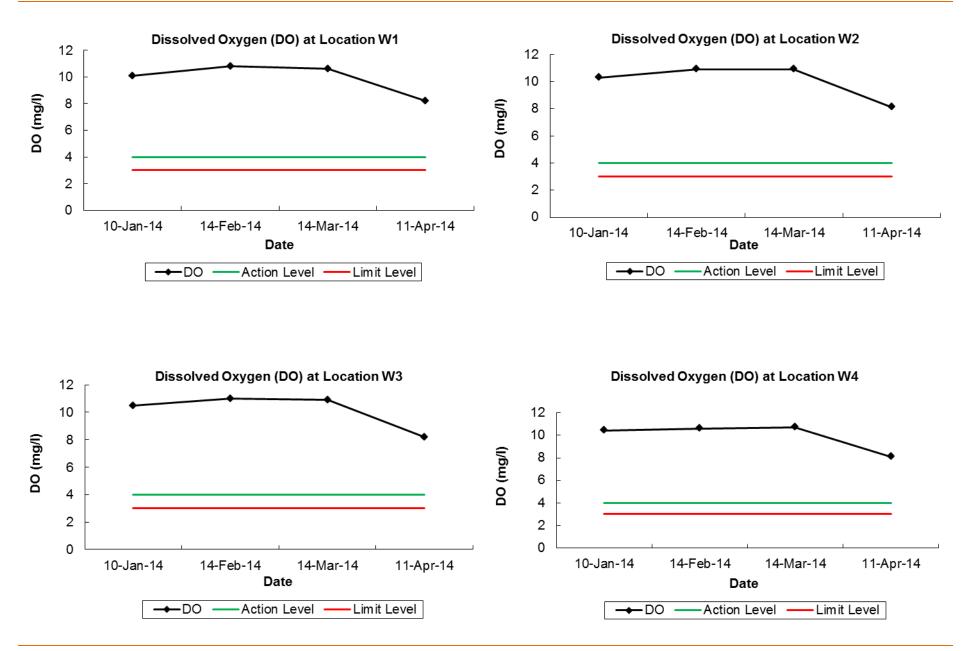


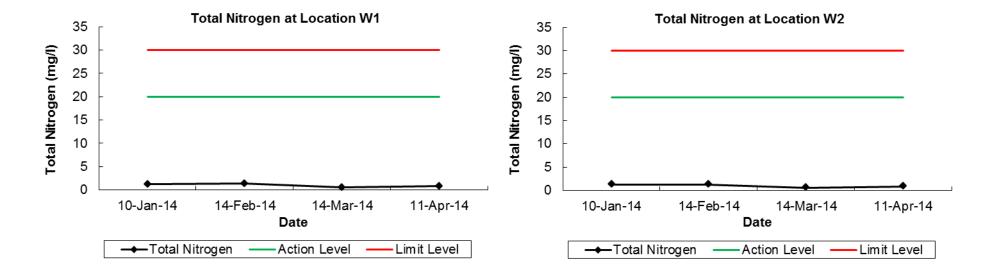


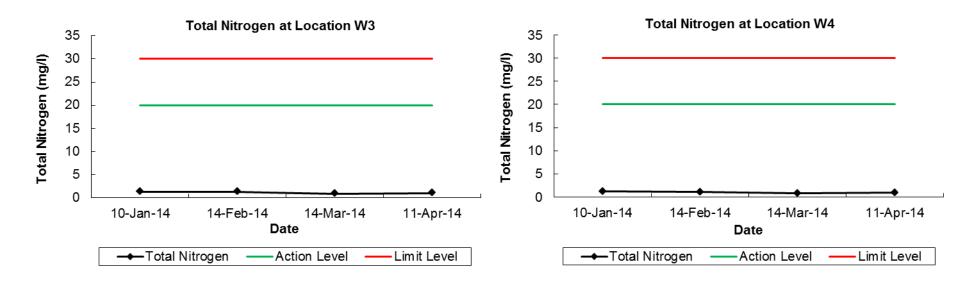

z:\jobs\j481c - skycity nine eagles golf course - em&a (2011-2012)\07 submission\2014\feb-apr14\d01-16 em&a report (feb-apr14)_r1.docx

SMEC

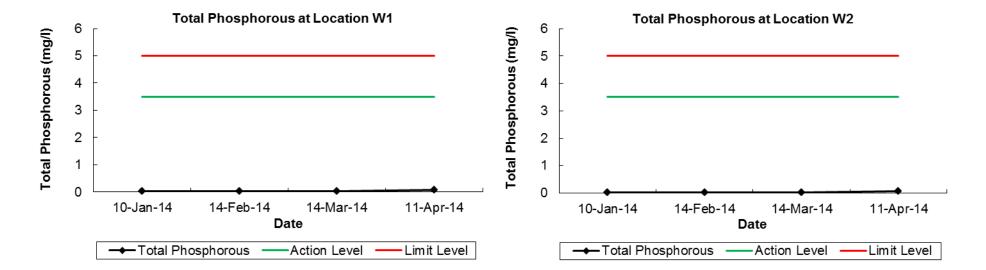

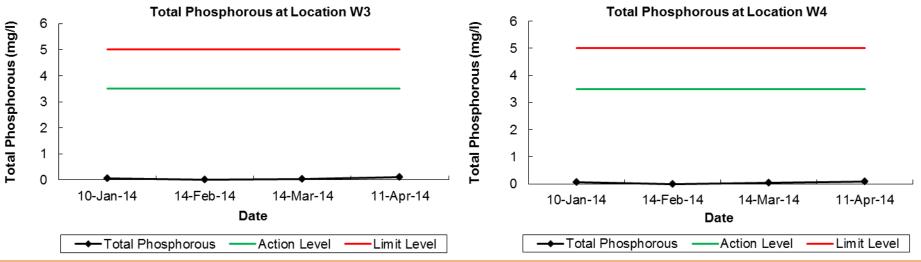





APPENDIX 4

Aqua Bio-Trol Liquid – Product Datasheet

Aqua Bio-Trol Liquid

Liquid Microbial Pond Clarifier

PRODUCT DATA BULLETIN

Features

- Eliminates pond scum and green, soupy conditions
- Improves water clarity
- Reduces foul odors and organic sediment
- Contains facultative bacteria capable of withstanding low oxygen levels
- Reduces levels of harmful nitrates & ammonia
- Effective under a wide range of climactic conditions
- Enhances conditions for all aquatic life
- Reduces biological oxygen demand
- Non-toxic, safe for fish, plants & applicator
- Microencapsulated, microbial stimulants

Aqua Bio-Trol Liquid is the safe, natural way to establish and maintain cleaner pond and lake water without chemicals. *Aqua Bio-Trol Liquid* eliminates pond scum and green, *soupy* conditions, while eliminating foul odors. *Aqua Bio-Trol Liquid* improves water clarity and digests excess organic matter in ponds, lakes and fountains.

Aqua Bio-Trol Liquid helps to create and maintain a healthier pond, lake and fountain water ecosystem through non-chemical treatment. *Aqua Bio-Trol Liquid* is an all natural, microbial based product effective for improving poor water conditions, and especially for maintenance of healthy water conditions once they are established. *Aqua Bio-Trol Liquid* is a concentration of naturally occurring microbes, which act to bring pond and lake water into proper ecological balance.

Aqua Bio-Trol Liquid is completely biodegradable and non-toxic to humans, animals and water life. The result of treatment is reduced organic sediment and particulate, reduced sludge, clear water, and enhanced conditions for all aquatic life.

Aqua Bio-Trol Liquid microbes preemptively consume organic matter which feeds algae and which leads to anaerobic conditions, including bad odors. The active microbes in *Aqua Bio-Trol Liquid* feed on excess nutrients in the entire water column, from sludge at the bottom to suspended particulate, to green organic matter on the surface. Routine application helps keep water in it's best condition without the use of potentially harmful chemicals.



DIRECTIONS FOR USE

Aqua Bio-Trol Liquid is most effective when water temperatures range from 50° to 100° F. For best results, provide adequate surface or subsurface aeration. Subsuface aeration is preferred. For maximum efficiency, assure a minimum of 5-6 % dissolved oxygen.

Apply by distributing liquid as much as possible around pond and lake edges. Avoid dumping liquid in one location.

Pond	Initial	Monthly
Volume	Treatment	Maintenance
Acre Foot 325,900 gallons	4 gallons	2 gallons

Formulas to help in your calculations

- Length x Width x Depth (feet) x 7.48 = Number of Gallons
- One acre-foot of water = 325,900 gallons
- One acre-foot of water = 1,233 CuMt

Active Ingredients

A proprietary blend of 58 strains of aerobic and facultative beneficial bacteria at a minimum concentration of 6.6 x 10⁷ CFU per ml (including Bacillus subtilis)

Warranty: Seller warrants that the product conforms to its chemical description and is reasonably fit for the purpose stated on the label when used in accordance with directions under normal conditions of use; but neither this warranty nor any other warranty of merchantability or fitness of a particular product expressed or implied, extends to the use of this product contrary to label conditions, or under conditions not reasonably foreseeable to the seller; and buyer assumes the risk of any such use.

13802 Chrisman Road
Houston, Texas 77039 USA
800.442.9821 Fax 281.590.3353

Parkway Research A Division of BRANDT CONSOLIDATED

www.parkwayresearch.com • www.brandtconsolidated.com
