

Hip Hing – Ngo Kee Joint Venture

Hong Kong Convention and
Exhibition Centre Expansion
(Previously known as HKCEC
Atrium Link Extension):
*Monthly Environmental Monitoring
and Audit Report for September 2006*

October 2006

Environmental Resources Management

21/F Lincoln House
979 King's Road
Taikoo Place
Island East, Hong Kong
Telephone: (852) 2271 3000
Facsimile: (852) 2723 5660
E-mail: post.hk@erm.com
<http://www.erm.com>



ENVIRONMENTAL MONITORING &
AUDIT REPORT

Hip Hing – Ngo Kee Joint Venture

Hong Kong Convention and
Exhibition Centre Expansion
(Previously known as HKCEC
Atrium Link Extension):
*Monthly Environmental Monitoring
and Audit Report for September 2006*

13th October 2006

Reference 0050690

For and on behalf of Environmental Resources Management	
Approved by:	Steve Duckworth
Signed:	
Position:	Deputy Managing Director
Certified by:	 (Environmental Team Leader – Marcus Ip)
Date:	13 October 2006

This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



NATURE & TECHNOLOGIES (HK) LIMITED
科技環保(香港)有限公司

Unit 2 & 3, 4/F., Wellborne Commercial Centre, 8 Java Road, North Point, Hong Kong.
香港北角渣華道8號威邦商業中心4樓2及3室 Tel電話 : (852) 2877 3122 Fax傳真 : (852) 2511 0922
Email電郵: enquiry@nt.com.hk Web page網址 : http://www.nt.com.hk

Our Ref: 3.16/014/2006/it

14 October 2006

Maunsell Consultants Asia Ltd
Grand Central Plaza, Tower 2
138 Shatin Rural Committee Road
Shatin, N.T., Hong Kong

Attn: Ms Vera Chan

Dear Sir/Madam,

Hong Kong Convention Center Expansion (Previously known as Hong Kong Convention and Exhibition Center, Atrium Link Extension)
Monthly EM&A Report for September 2006
(Environmental Permit No. EP-239/2006)

With reference to the captioned document concerning the Monthly EM&A report for September 2006 received from ERM dated 13 October 2006, we are pleased to provide our verification for the document pursuant to condition 3 of the Environmental Permit (EP) No. EP-239/2006.

In future reports, it is recommended to include a list of submission status under the environmental permit as per paragraph 8.9(ii) of the EM&A Manual.

Yours faithfully,
Nature & Technologies (HK) Limited

Ir Dr Gabriel C K Lam
Managing Director

- cc: - Hong Kong Trade Development Council (Attn: Mr. K. F. Chan)
- Hip Hing Ngo Kee Joint Venture (Attn: Mr. Eric Lau & Mr. William Tam)
- ERM (Attn: Mr. Marcus Ip)

CONTENTS

	<i>EXECUTIVE SUMMARY</i>	<i>I</i>
<i>1</i>	<i>INTRODUCTION</i>	<i>1</i>
<i>1.1</i>	<i>PURPOSE OF THE REPORT</i>	<i>1</i>
<i>1.2</i>	<i>STRUCTURE OF THE REPORT</i>	<i>1</i>
<i>2</i>	<i>PROJECT INFORMATION</i>	<i>3</i>
<i>2.1</i>	<i>BACKGROUND</i>	<i>3</i>
<i>2.2</i>	<i>SITE DESCRIPTION</i>	<i>3</i>
<i>2.3</i>	<i>CONSTRUCTION ACTIVITIES</i>	<i>4</i>
<i>2.4</i>	<i>PROJECT ORGANISATION</i>	<i>4</i>
<i>2.5</i>	<i>STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS</i>	<i>4</i>
<i>3</i>	<i>ENVIRONMENTAL MONITORING METHODOLOGY</i>	<i>6</i>
<i>3.1</i>	<i>AIR QUALITY MONITORING</i>	<i>6</i>
<i>3.2</i>	<i>WATER QUALITY MONITORING</i>	<i>9</i>
<i>4</i>	<i>IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS</i>	<i>12</i>
<i>5</i>	<i>MONITORING RESULTS</i>	<i>13</i>
<i>5.1</i>	<i>AIR QUALITY</i>	<i>13</i>
<i>5.2</i>	<i>WATER QUALITY</i>	<i>13</i>
<i>5.3</i>	<i>WASTE MANAGEMENT</i>	<i>13</i>
<i>6</i>	<i>ENVIRONMENTAL SITE AUDITING</i>	<i>14</i>
<i>7</i>	<i>ENVIRONMENTAL NON-CONFORMANCE</i>	<i>16</i>
<i>7.1</i>	<i>SUMMARY OF MONITORING EXCEEDANCE</i>	<i>16</i>
<i>7.2</i>	<i>SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE</i>	<i>16</i>
<i>7.3</i>	<i>SUMMARY OF ENVIRONMENTAL COMPLAINT</i>	<i>16</i>
<i>7.4</i>	<i>SUMMARY OF ENVIRONMENTAL SUMMONS AND PROSECUTION</i>	<i>16</i>
<i>8</i>	<i>FUTURE KEY ISSUES</i>	<i>17</i>
<i>8.1</i>	<i>KEY ISSUES FOR THE COMING MONTH</i>	<i>17</i>
<i>8.2</i>	<i>MONITORING SCHEDULE FOR THE COMING MONTHS</i>	<i>17</i>
<i>8.3</i>	<i>CONSTRUCTION PROGRAMME FOR THE NEXT THREE MONTHS</i>	<i>17</i>
<i>9</i>	<i>REVIEW OF THE EM&A DATA AND EIA PREDICTIONS</i>	<i>18</i>
<i>9.1</i>	<i>AIR QUALITY</i>	<i>18</i>
<i>9.2</i>	<i>WATER QUALITY</i>	<i>18</i>
<i>9.3</i>	<i>WASTE MANAGEMENT</i>	<i>18</i>

9.4	CONCLUSION OF REVIEW	19
10	CONCLUSION	20

LIST OF TABLES

Table 2.1	Summary of Construction Activities Undertaken from 1 September 2006 to 30 September 2006
Table 2.2	Summary of Environmental Licensing, Notification and Permit Status
Table 3.1	Air Monitoring Stations
Table 3.2	TSP Monitoring Parameter and Frequency
Table 3.3	Action and Limit Levels for Air Quality
Table 3.4	TSP Monitoring Equipment
Table 3.5	Water Quality Monitoring Locations
Table 3.6	Water Quality Monitoring Parameters & Frequency
Table 3.7	Action and Limit Levels for Water Quality
Table 5.2	Quantities of Waste Generated from the Project
Table 6.1	Results of Water Sampling at Discharge Point 1 and 2
Table 7.1	Statistical Summary of Environmental Complaint
Table 8.1	Construction Works to be Undertaken in the Coming Month
Table 9.1	Comparison of the Predicted and Monitoring Results of Air Quality Monitoring
Table 9.2	Comparison of the Estimated Amount and the Actual Amount of Waste Generated

LIST OF ANNEXES

Annex A	Location of Works Areas
Annex B	Location of Construction Activities during the Reporting Month
Annex C	Project Organization Chart and Contact Detail
Annex D	Locations of Monitoring Stations
Annex E	Monitoring Schedule in September to November 2006
Annex F	Calibration Reports for HVSs
Annex G	Event / Action Plans for Air and Water Quality Monitoring
Annex H	Summary of Implementation Status
Annex I	24-hour TSP Monitoring Results
Annex J	Laboratory Report of Water Quality Sampling
Annex K	Waste Flow Table
Annex L	Construction Programme for Next Three Months

EXECUTIVE SUMMARY

The construction works for Hong Kong Convention and Exhibition Centre Expansion (previously known as HKCEC Atrium Link Extension) (EIAO Register No: AEIAR-100/2006) was commenced on 1 August 2006. This is the second monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 September 2006 to 30 September 2006 in accordance with the EM&A Manual.

Summary of Construction Works undertaken during the Reporting Period

The major construction works taken during the reporting period were mobilization and commencement of pre-bored H-piles installation; demolition of abandoned water pump room; mobilization of percussion drill; and mini piling works to prepare subsequent installation of temporary marine work platform.

Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

24-hour & 1-hour Total Suspended	
Particulates (TSP) monitoring	5 times
Joint environmental site auditing	4 times

Air Quality

Five sets of 24-hour and fifteen sets of 1-hour TSP monitoring were carried out at the designated monitoring stations (AM1 & AM2) during the reporting period. No exceedance was recorded during the reporting month.

Water Quality

No installation and removal of temporary marine piles was undertaken during the reporting month and therefore water quality monitoring was not conducted.

Construction Waste Management

Wastes from this Project include inert construction and demolition (C&D) wastes and non-inert C&D wastes. A total of 1,509 tonnes of inert C&D wastes including 2 tonnes materials reused in this Project and 276 tonnes of non-inert C&D materials were generated during the reporting period. The non-inert C&D wastes and inert C&D materials generated from the Project were disposed of at SENT Landfill and public fill barging point at Quarry Bay respectively.

Environmental Site Auditing

Four weekly joint environmental site audits were carried out by the ET. Details of the audit findings and implementation status are presented in *Section 6*.

Bi-monthly water quality sampling was conducted and the results indicate that the treated effluent discharged from the Project was in compliance with the requirement of the relevant discharge licence issued under the Water Pollution Control Ordinance (WPCO).

Environmental Non-conformance

No environmental non-compliance was identified during the reporting period.

No environmental complaint or summons was received during the reporting period.

Future Key Issues

Works to be taken in the coming monitoring period are foundation work and bored piling preparation work.

Potential environmental impacts arising from the construction activities in the coming month are mainly associated with dust, site runoff, marine water quality and waste.

ERM-Hong Kong, Limited (ERM) was appointed by Hip Hing – Ngo Kee Joint Venture as the Environmental Team (ET) to implement the Environmental Monitoring and Audit (EM&A) programme for Contract No. H200605 of Hong Kong Convention and Exhibition Centre Expansion (previously known as HKCEC Atrium Link Extension) (the Project).

1.1 PURPOSE OF THE REPORT

This is the second EM&A report which summarizes the impact monitoring results and audit findings for the EM&A programme during the reporting period from **1 September 2006 to 30 September 2006**.

1.2 STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1 : Introduction

details the scope and structure of the report.

Section 2 : Project Information

summarizes background and scope of the Project, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permits/Licences during the reporting period.

Section 3 : Environmental Monitoring Requirement

summarizes the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels and Event / Action Plans.

Section 4 : Implementation Status on Environmental Mitigation Measures

summarizes the implementation of environmental protection measures during the reporting period.

Section 5 : Monitoring Results

summarizes the monitoring results obtained in the reporting period.

Section 6 : Environmental Site Auditing

summarizes the audit findings of the weekly site inspections undertaken within the reporting period.

Section 7 : **Environmental Non-conformance**

summarizes any monitoring exceedance, environmental complaints and environmental summons within the reporting period.

Section 8 : **Future Key Issues**

summarizes the impact forecast and monitoring schedule for the next three months.

Section 9 : **Review of EM&A Data and EIA Predictions**

compares and contrasts the EM&A data in the month with the EIA predictions and annotates with explanation for any discrepancies.

Section 10 : **Conclusions**

2.1 BACKGROUND

The Hong Kong Trade Development Council (HKTDC) is expanding its existing facilities to provide additional space for Hong Kong's leading trade fairs to be held at the Hong Kong Convention and Exhibition Centre (HKCEC). The Project is located in the North Wan Chai and will occupy the aerial space between Phase I and Phase II of the HKCEC. The new Atrium Link Extension (ALE) will span across the water channel between Phase I and Phase II of the HKCEC to accommodate 3 main levels of Exhibition Hall Extensions. The level of the main roof of the Extension will be of similar height as that of the podium roof of the Phase I building. A northern row of permanent supporting columns will be located on land close to Expo Drive Central and similarly a southern row will land near to Convention Avenue. There will be no permanent intermediate columns in the waterway.

The major works activities for the ALE will comprise the following:

- Construction and demolition of the temporary footbridge;
- Demolition of the existing Atrium Link;
- Construction and demolition of a temporary working platform;
- Construction of foundations and pile caps for the ALE; and
- Construction of superstructure for the ALE.

The potential environmental impacts of the Project have been studied in the "*Hong Kong Convention and Exhibition Centre, Atrium Link Extension – Environmental Impact Assessment Report*" (EIAO Register No: AEIAR-100/2006). The EIA was approved on 21 April 2006 under the *Environmental Impact Assessment Ordinance* (EIAO) and an Environmental Permit (EP-239/2006) for the works was granted on 12 May 2006. Under the requirements of Condition 3.1 of Environmental Permit EP-239/2006, EM&A programme as set out in the EM&A Manual is required to be implemented.

The construction works commenced on 1 August 2006 and are scheduled to be completed by March 2009.

2.2 SITE DESCRIPTION

The works areas of the Project are illustrated in *Annex A*.

2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1*. The locations of the construction activities are shown in *Annex B*.

Table 2.1 *Summary of Construction Activities Undertaken from 1 September 2006 to 30 September 2006*

Construction Activities Undertaken
<ul style="list-style-type: none">• Preparation work for demolition• Mobilization for pre-bored H-piles• Pre-bored H-piles at southern and northern sides• Demolition of abandoned water pump room• Mobilization of percussion drill for bored piling at the southern side• Mini piles to prepare for temporary marine work platform at the southern side• Internal hoarding erection for demolition works• Preparation work for dismantling of curtain wall• E&M diversion at northern side

2.4 PROJECT ORGANISATION

The Project organisation chart and contact details are shown in *Annex C*.

2.5 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since August 2006 is presented in *Table 2.2*.

Table 2.2 *Summary of Environmental Licensing, Notification and Permit Status*

Permit/ Licenses/ Notification	Reference	Validity Period	Remarks
Environmental Permit	EP-239/2006	Throughout the Contract	Permit granted on 12 May 2006
Notification of Construction Works under Air Pollution Control (Construction Dust) Regulation	--	--	Notification on 23 June 2006
Discharge Licence under Water Pollution Control Ordinance	EP860/W10/XY0145	N/A	-
Chemical Waste Producer Registration	WPN5213-134-H3125-01	N/A	Chemical waste types: spent paint, acid, alkaline, adhesive, diesel fuel, lubricating oil and bitumen.

Permit/ Licenses/ Notification	Reference	Validity Period	Remarks
Construction Noise Permit for area inside the Atrium Link	GW-RS0429-06	Valid from 25 July 2006 and will be expired on 23 December 2006	-
	GW-RS0487-06	Valid from 21 August 2006 and will be expired on 30 December 2006	-
	GW-RS0511-06	Valid from 29 August 2006 and will be expired on 27 October 2006	-
	GW-RS0535-06	Valid from 11 September 06 and will be expired on 30 January 07)	
	PP-RS0028-06	Valid from 14 September 06 and expired 14 November 06	

3.1 AIR QUALITY MONITORING

3.1.1 Monitoring Location

In accordance with the EM&A Manual, 24-hour and 1-hour Total Suspended Particulates (TSP) levels was conducted at the monitoring stations listed in *Table 3.1*. Map and photographs showing the monitoring stations are presented in *Annex D*.

Table 3.1 *Air Monitoring Stations*

Monitoring Station	Description
AM1	Pedestrian Plaza
AM2	Renaissance Harbour View Hotel Hong Kong

3.1.2 Monitoring Parameters, Frequency and Programme

Air quality monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual (*Table 3.2*). The monitoring programme for this and next three reporting period is shown in *Annex E*.

Table 3.2 *TSP Monitoring Parameter and Frequency*

Parameter	Frequency
24-hour TSP	Once per day for 14 days
1-hour TSP	3 times per day for 14 days

3.1.3 Action and Limit Levels

The Action and Limit levels were established in accordance with the EM&A Manual and are presented in *Table 3.3*.

Table 3.3 *Action and Limit Levels for Air Quality*

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
24-hour TSP	AM1	161	260
	AM2	168	260
1-hour TSP	AM1	327	500
	AM2	329	500

3.1.4 Monitoring Equipment

Continuous 24-hour and 1-hour TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring station. The performance specification of HVS complies with the standard method “*Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)*” as stipulated in US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B).

Table 3.4 summarizes the equipment that was used in the 24-hour and 1-hour TSP monitoring.

Table 3.4 ***TSP Monitoring Equipment***

Monitoring Station	Equipment	Model (HVS, Calibration Kit)
AM1 (for 24-hr TSP)	HVS, Calibration Kit	GMW-9503, Tisch TE-5025 A
AM2 (for 24-hr TSP)	HVS, Calibration Kit	GMW-9795, Tisch TE-5025A
AM1 (for 1-hr TSP)	HVS, Calibration Kit	GMW-9864, Tisch TE-5025A
AM2 (for 1-hr TSP)	HVS, Calibration Kit	GMW-8115, Tisch TE-5025 A

3.1.5 ***Monitoring Methodology***

Installation

The HVSs at AM1 and AM2 were placed at about 1.3 m above local ground level and about 4.3 m above local ground respectively. All of the HVSs were free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- horizontal platform with appropriate support to secure the samplers against gusty wind were provided at AM1 & AM2;
- a minimum of 2 m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues were nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

Preparation of Filter Papers by ETS-Test Consultant Ltd

- glass fibre filters were labeled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ± 3 °C; the relative humidity (RH) was 40%; and
- ETS-Test Consultant Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

Field Monitoring

- the power supply was checked to ensure that the HVSs were working properly;
- the filter holder and the area surrounding the filter were cleaned;

- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- then the shelter lid was closed and secured with the aluminum strip;
- the HVSs were warmed-up for about 5 minutes to establish run-temperature conditions;
- a new flowrate record sheet was set into the flow recorder;
- the flow rate of the HVSs was checked and adjust at around 0.6 -1.44 m³/min. The range specified in the EM&A Manual was between 0.6 – 1.7 m³/min;
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact;
- it was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to ETS-Test Consultant Ltd for analysis.

3.1.6 *Maintenance and Calibration*

The HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.

The flow rate of each HVS with mass flow controller were calibrated using an orifice calibrator. Initial calibration of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using Tisch TE-5025 A Calibration Kit. The calibration records for the HVSs are given in *Annex F*.

3.1.7 *Event Action Plan*

The Event / Action Plan (EAP) for air quality monitoring is presented in *Annex G*.

3.2 *WATER QUALITY MONITORING*

3.2.1 *Monitoring Location*

In accordance with the EM&A Manual, the marine water quality monitoring will be conducted at the monitoring stations during the installation and removal of temporary marine piles (*Table 3.5*). Map and photographs showing the monitoring stations are presented in *Annex D*.

Table 3.5 *Water Quality Monitoring Locations*

Station	Location	Intake Level	Easting	Northing
W3	Hong Kong Convention and Exhibition Centre Phase I Cooling Water Intake	7.5m below the existing pump house floor	835852.3	815907.0
W4	Wan Chai Tower/ Revenue Tower/ Immigration Tower Cooling Water Intake ⁽¹⁾	5m below the top of the existing sea wall	835944.1	815885.0
W5	Great Eagle Centre, China Resources Building Cooling Water Intake	5m below the top of the existing sea wall	835963.4	815886.5

Note:
(1) The cooling water intake for Wan Chai Tower / Revenue Tower/ Immigration Tower will be partially relocated to the new pump house adjacent to Station W3 tentatively in September 2006.

3.2.2 *Monitoring Parameters, Frequency and Programme*

The water quality monitoring will be conducted in accordance with *Table 3.6* during the period of installation and removal of temporary marine piles.

Table 3.6 *Water Quality Monitoring Parameters & Frequency*

Parameter	Frequency	No. of Samples per Monitoring Event	Duration
Dissolved Oxygen (DO) Suspended Solids (SS) Turbidity	3 days per week at mid-flood & mid-ebb tides	2	During installation and removal of temporary marine piles.

Reference will be made to the predicted tides at Quarry Bay, which is the tidal station nearest to the Project Site, published on the web site of Hong Kong Observatory (<http://www.hko.gov.hk/tide/eQUBtide.htm>).

Measurements of suspended solids (SS), turbidity in Nephelometric Turbidity Units (NTU) and dissolved oxygen (DO) in mgL⁻¹ shall be undertaken at designated monitoring stations. The first parameter shall be determined in the laboratory with the latter three shall be measured in-situ.

3.2.3 *Action and Limit Levels*

The Action and Limit levels were established in accordance with the EM&A Manual and are presented in *Table 3.7*.

Table 3.7 Action and Limit Levels for Water Quality

Parameter	Tide	Action Level	Limit Level
Dissolved Oxygen (DO) in mgL ⁻¹	Mid-Ebb	3.26	3.23
	Mid-Flood	3.25	3.14
Suspended Solids (SS) in mgL ⁻¹	Mid-Ebb	9.00	10.00
	Mid-Flood	8.18	8.40
Turbidity (Tby) in NTU	Mid-Ebb	5.32	6.19
	Mid-Flood	4.76	5.79

3.2.4 *Monitoring Equipment and Methodology*

Dissolved oxygen and temperature measuring equipment

The portable and weatherproof dissolved oxygen (DO) measuring meter (YSI Model 85) will be used in the impact monitoring.

The DO measuring meter has a membrane electrode with automatic temperature compensation complete with a 50-feet cable. Wet bulb calibration for a DO meter will be carried out before measurement at each monitoring station.

Turbidity Measurement Instrument

The turbidity measurements will be carried out on split water sample collected from the same depths of SS samples. A portable and weatherproof turbidity-measuring meter (HACH model 2100P) will be used in the impact monitoring. It has a photoelectric sensor capable of measuring turbidity between 0-1000 NTU. Response of the sensor will be checked with certified standard turbidity solutions before the start of measurement.

Suspended Solids

Water samples for suspended solids measurement will be collected by use of a transparent PVC cylinder (Kahlsico Water Sampler), packed in ice (cooled to 4°C without being frozen) and delivered to the laboratory as soon as possible after collection. The SS determination work will be started within 24 hours after the collection of the water samples, and the testing method of SS will be carried by ETS-Testconsult Ltd (HOKLAS accredited laboratory) in accordance with the APHA 19ed 2540D⁽¹⁾ and the lowest detection limit is 1 mgL⁻¹. The Quality Assurance/Quality Control (QA/QC) procedures will be followed as required by HOKLAS.

⁽¹⁾ American Public Health Association Standard Methods for the Examination of Water and Wastewater.

Water Depth Detector

A portable, battery-operated echo sounder (Speedtech instrument SM-5A) will be used for the determination of water depth at each designated monitoring station.

Salinity

A portable salinometer (YSI Model 85) capable of measuring salinity in the range of 0 - 40 ppt will be used to measure the salinity of the marine water at monitoring stations. It will be checked with 30ppt Salinity solutions before the start of the measurement.

Location of the Monitoring Sites

A hand-held GPS (MLR SP24) and together with a suitably scaled map will be used for locating the water quality monitoring stations.

Calibration of Equipment

All in-situ monitoring instruments will be checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout the water quality monitoring.

3.2.5

Event / Action Plan

The Event / Action Plan (EAP) for water quality monitoring is presented in ***Annex G***.

IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS

The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Report, the Environmental Permit and EM&A Manual. The implementation status and status of required submissions under the EP during the reporting period is summarized in *Annex H*.

5.1 AIR QUALITY

The monitoring data at AM1 and AM2 are provided by ETS-Testconsult Ltd. Five sets of 24-hour and fifteen sets of 1-hour TSP monitoring were carried out at the designated monitoring stations (AM1 & AM2) during the reporting period. The monitoring data for 24-hour TSP and 1-hour TSP together with wind data and graphical presentations are presented in *Annex I*.

The weather condition during the monitoring period varied from sunny to rainy. The local impacts observed near the monitoring stations were mainly vehicle emissions along Convention Avenue and Fleming Road.

5.2 WATER QUALITY

In accordance with Section 4.11 of the EM&A Manual, water quality monitoring shall be conducted during the period of installation and removal of temporary marine piles. Since there was no such work undertaken during the reporting month, no water quality monitoring was conducted.

5.3 WASTE MANAGEMENT

Wastes from this Project include inert construction and demolition (C&D) wastes and non-inert C&D wastes. Reference has been made on the Monthly and Yearly Summary Waste Flow Table prepared by Hip Hing – Ngo Kee Joint Venture (*Annex K*). With reference to relevant handling records and trip tickets of this Project, the quantities of different wastes are summarized in *Table 5.1*.

Table 5.1 Quantities of Waste Generated from the Project

Month/ Year	Quantity	
	C&D Materials (inert) ^(a)	C&D Materials (non-inert) ^(b)
August 2006	264 tonnes	132 tonnes
September 2006	1,509 tonnes	276 tonnes
Total	1,773 tonnes	408 tonnes

Notes:

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 2 tonnes of inert C&D materials were reused either in this Project. Non-reused inert C&D materials were disposed at the public fill barging point at Quarry Bay.

(b) Non-inert C&D materials include steel materials generated from demolition of footbridge, the existing Atrium Link and working platform, paper / cardboard packaging waste, chemical waste and other wastes such as general refuse. Non-inert C&D material were disposed at SENT Landfill.

Weekly site inspections were carried out by the ET. Five site inspections were conducted on 6, 15, 20 and 27 September 2006. There was no non-compliance event recorded in the reporting month.

Major findings and recommendations are summarized as follows:

Site Specific

- (i) It is recommended to remove silt frequently and to maintain good de-silting performance of the wheel washing bay. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (ii) A small amount of sand was observed on the public road surface outside the West Site Entrance. Since this Site Entrance is reportedly not accessible because of the limited space occurred by the drilling rigs, it was believed that the sand was dropped from the skip hoist during transportation. It is recommended to clean the road surface and aware of leaking during material transport. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (iii) It is recommended to stop the leakage and provide drip tray underneath the air compressor. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (iv) It is recommended to store the lubricate oil containers inside chemical storage room or drip trays on-site. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (v) It is recommended to remove oil stains near West Site Entrance of the southern side of the Site. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (vi) It is recommended to provide drip tray for all oil containers. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (vii) It is recommended to regularly remove the soil accumulated at the piling area in order to avoid overflowing of soil and silty water outside the site area. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (viii) It is recommended to regularly pump the site runoff accumulated within the southern side of the Site to the wastewater treatment plant. The corrective action was undertaken as observed in the site audit conducted in the reporting period.

- (ix) It is recommended to well maintain and clean the site area regularly. The corrective action was undertaken as observed in the site audit conducted in the reporting period.
- (x) It is recommended to provide earth bund / concrete bund at the southern boundary of work area located at southern side of the Site in order to avoid site runoff entering the storm drains at Convention Avenue. The corrective action was undertaken as observed in the site audit conducted in the reporting period.

General

- (xi) It is recommended to prepare waste disposal recording system in accordance with *Annex 2, Appendix A of the Environment, Transport and Works Bureau Technical Circular (Works) No. 31/2004*. A trip ticket system has been set up by the Contractor in the reporting period.
- (xii) Waste Management Plan was prepared by the Contractor in accordance with *Environment, Transport and Works Bureau Technical Circular (Works) No. 19/2005*.

Water Discharge Sampling

In accordance with the discharge licence issued under WPCO, water sampling should be conducted quarterly to ensure the quality of treated effluent complying with the requirements of discharge license. The Contractor proposed to conduct the water sampling on a bi-monthly basis. Water quality sampling at Discharge Points 1 and 2 was conducted on 7 September 2006, and water quality sampling at Discharge Point 3 will be conducted in October 2006. *Table 6.1* shows that the effluent discharged from the project was in compliance with the discharge limit stipulated in the Water Discharge License. The laboratory testing reports of the water sampling are presented in *Annex J*.

Table 6.1 ***Results of Water Sampling at Discharge Point 1 and 2***

Parameter	Test Result	Discharge Limit
<i>Discharge Point 1 ⁽¹⁾</i>		
pH	7.0	6-9
Total Suspended Solids (TSS) Dried at 103-105°C (mg/L)	17	≤30
Chemical Oxygen Demand (COD) (mgO ₂ /L)	<50	≤80
<i>Discharge Point 2 ⁽²⁾</i>		
pH	7.4	6-9
Total Suspended Solids (TSS) Dried at 103-105°C (mg/L)	8.8	≤30
Chemical Oxygen Demand (COD) (mgO ₂ /L)	<50	≤80
Note: ⁽¹⁾ Discharge point 1 is the gully located at the east end of Expo Drive Central.		
⁽²⁾ Discharge point 2 is the gully located at the west end of Expo Drive Central.		

7 ENVIRONMENTAL NON-CONFORMANCE

7.1 SUMMARY OF MONITORING EXCEEDANCE

No exceedance of the Action and Limit Levels of 24-hour TSP was recorded at monitoring stations during the reporting period.

7.2 SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE

No non-compliance event was recorded during the reporting period.

7.3 SUMMARY OF ENVIRONMENTAL COMPLAINT

No complaint was received during the reporting period. A statistical summary of environmental complaints since project commencement is presented in *Table 7.2*.

Table 7.1 Statistical Summary of Environmental Complaint

Reporting Period	Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1/8/06 – 31/08/06	0	0	-
1/9/06 – 30/09/06	0	0	-

7.4 SUMMARY OF ENVIRONMENTAL SUMMONS AND PROSECUTION

There was no summons or prosecution on environmental matters during the reporting period.

8.1 KEY ISSUES FOR THE COMING MONTH

Works to be taken for the coming monitoring period are summarized in *Table 8.1*.

Table 8.1 Construction Works to be Undertaken in the Coming Month

Work to be taken
<ul style="list-style-type: none"> • Bored piling preparing work • Mobilization and relocation of prebored H-pile • Foundation work - Pre-bored H-pile Piling works • Mini piles for temporary marine work platform • Phase I marine piling work • Preparation of demolition works

Potential environmental impacts arising from the above construction activities are mainly associated with dust, site runoff and waste management.

8.2 MONITORING SCHEDULE FOR THE COMING MONTHS

The tentative schedule of TSP monitoring for the next three months is presented in *Annex E*. The environmental monitoring will be conducted at the same monitoring locations in this reporting month. It is anticipated that the installation of temporary marine piles may be carried out in mid-October 2006 and the water monitoring will be conducted during the installation of temporary marine piles (*Annex E*). The monitoring programme has been reviewed and was considered as adequate to cater the nature of works in progress.

8.3 CONSTRUCTION PROGRAMME FOR THE NEXT THREE MONTHS

The construction programme for the next three months is presented in *Annex L*.

9.1 AIR QUALITY

Since the EIA only have qualitative assessment of dust impact during construction phase, the comparison were made on monitoring results and the Hong Kong Air Quality Objectives (HKAQO) (*Table 9.1*).

Table 9.1 *Comparison of the Predicted and Monitoring Results of Air Quality Monitoring*

Monitoring Stations	Corresponding ASR in EIA	HKAQO, ug/m ³	Measured 24 hour TSP Monitoring Results, ug/m ³ ⁽²⁾	
		24 hour ⁽¹⁾	Average	Range
AM1	AM8	260	58	34 – 87
AM2	AM6	260	56	29 – 85

Remarks:

(1) Only 24 hours TSP monitoring results were compared as there is no maximum allowable concentration of 1 hour TSP in HKAQO.

(2) Average and range of data were calculated for the period of monitoring between August 2006 to September 2006

The monitoring results show that air quality impacts from construction activities during the reporting period are well below maximum allowable concentration stipulated in the HKAQO. Recommended mitigation measures in Section 4.24 of EIA were implemented during the reporting period and are regarded as effective.

9.2 WATER QUALITY

Since no water quality monitoring is required in the reporting period, review of EM&A data will be conducted in the future report.

9.3 WASTE MANAGEMENT

The estimated amount of waste generated in this project and the quantities of waste generated during the reporting period are presented in *Table 9.2*. Recommended mitigation measures in Section 6.35 to 6.41 of the EIA are implemented during the reporting period and regarded as effective.

Table 9.2 *Comparison of the Estimated Amount and the Actual Amount of Waste Generated*

Type of Material	Estimated Amount of C&D Materials in EIA (inert & non-inert)	Actual Amount of C&D Materials Recorded (inert & non-inert)
Demolition of temp. footbridge	585 tonnes	0
Demolition of existing Atrium Link	4,680 tonnes	0

Type of Material	Estimated Amount of C&D Materials in EIA (inert & non-inert)	Actual Amount of C&D Materials Recorded (inert & non-inert)
Demolition of temp. working platform	390 tonnes	0
Construction of foundations and pile caps	20,000 tonnes	2,071 tonnes
General Refuse	Insignificant	110 tonnes
Chemical Waste	Small	0

9.4

CONCLUSION OF REVIEW

The EIA predictions and the monitoring results during the reporting period have been reviewed. As the EIA predictions were based on worst scenarios of the construction activities, and therefore the EIA predictions were higher than the monitoring results.

It is concluded that there are no discrepancies observed between the EIA predictions and the monitoring results. Recommendations given in the EIA are also considered to be adequate and effective for minimising the environmental impacts.

The Environmental Monitoring and Audit (EM&A) Report presents the EM&A works undertaken during the period from 1 September to 30 September 2006 in accordance with EM&A Manual and the requirement under EP-239/2006.

There was no exceedance of the Action and Limit Levels of 24-hour and 1-hour TSP was recorded at the monitoring stations during the reporting month.

There was no non-compliance event was recorded during the reporting month

There was no complaint and summons/prosecution received during the reporting period.

The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Annex A

Locations of Works Areas


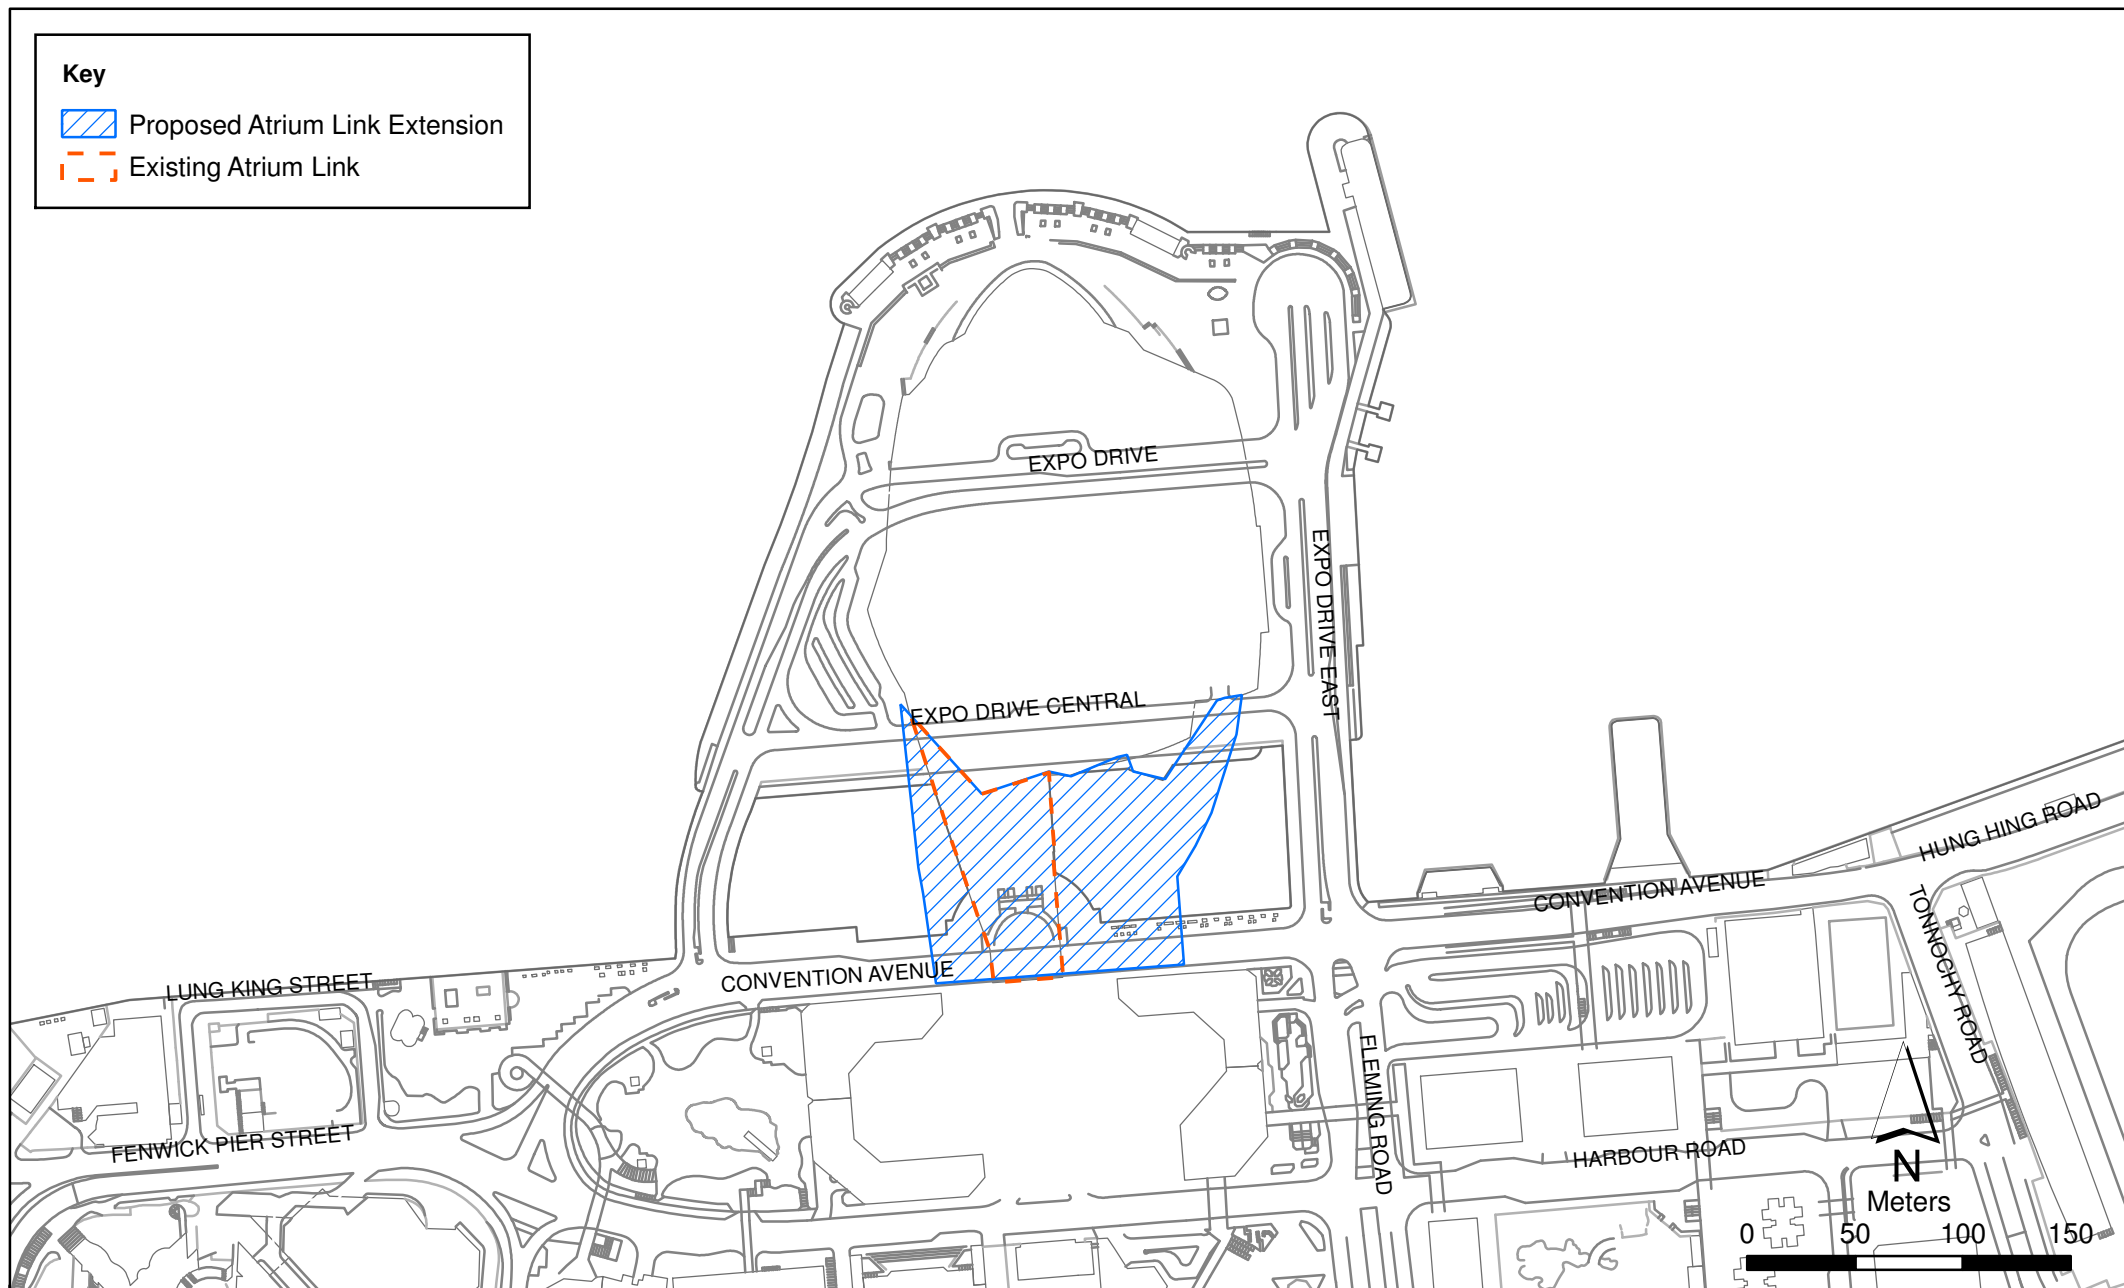


Figure A1

Location of Atrium Link Extension



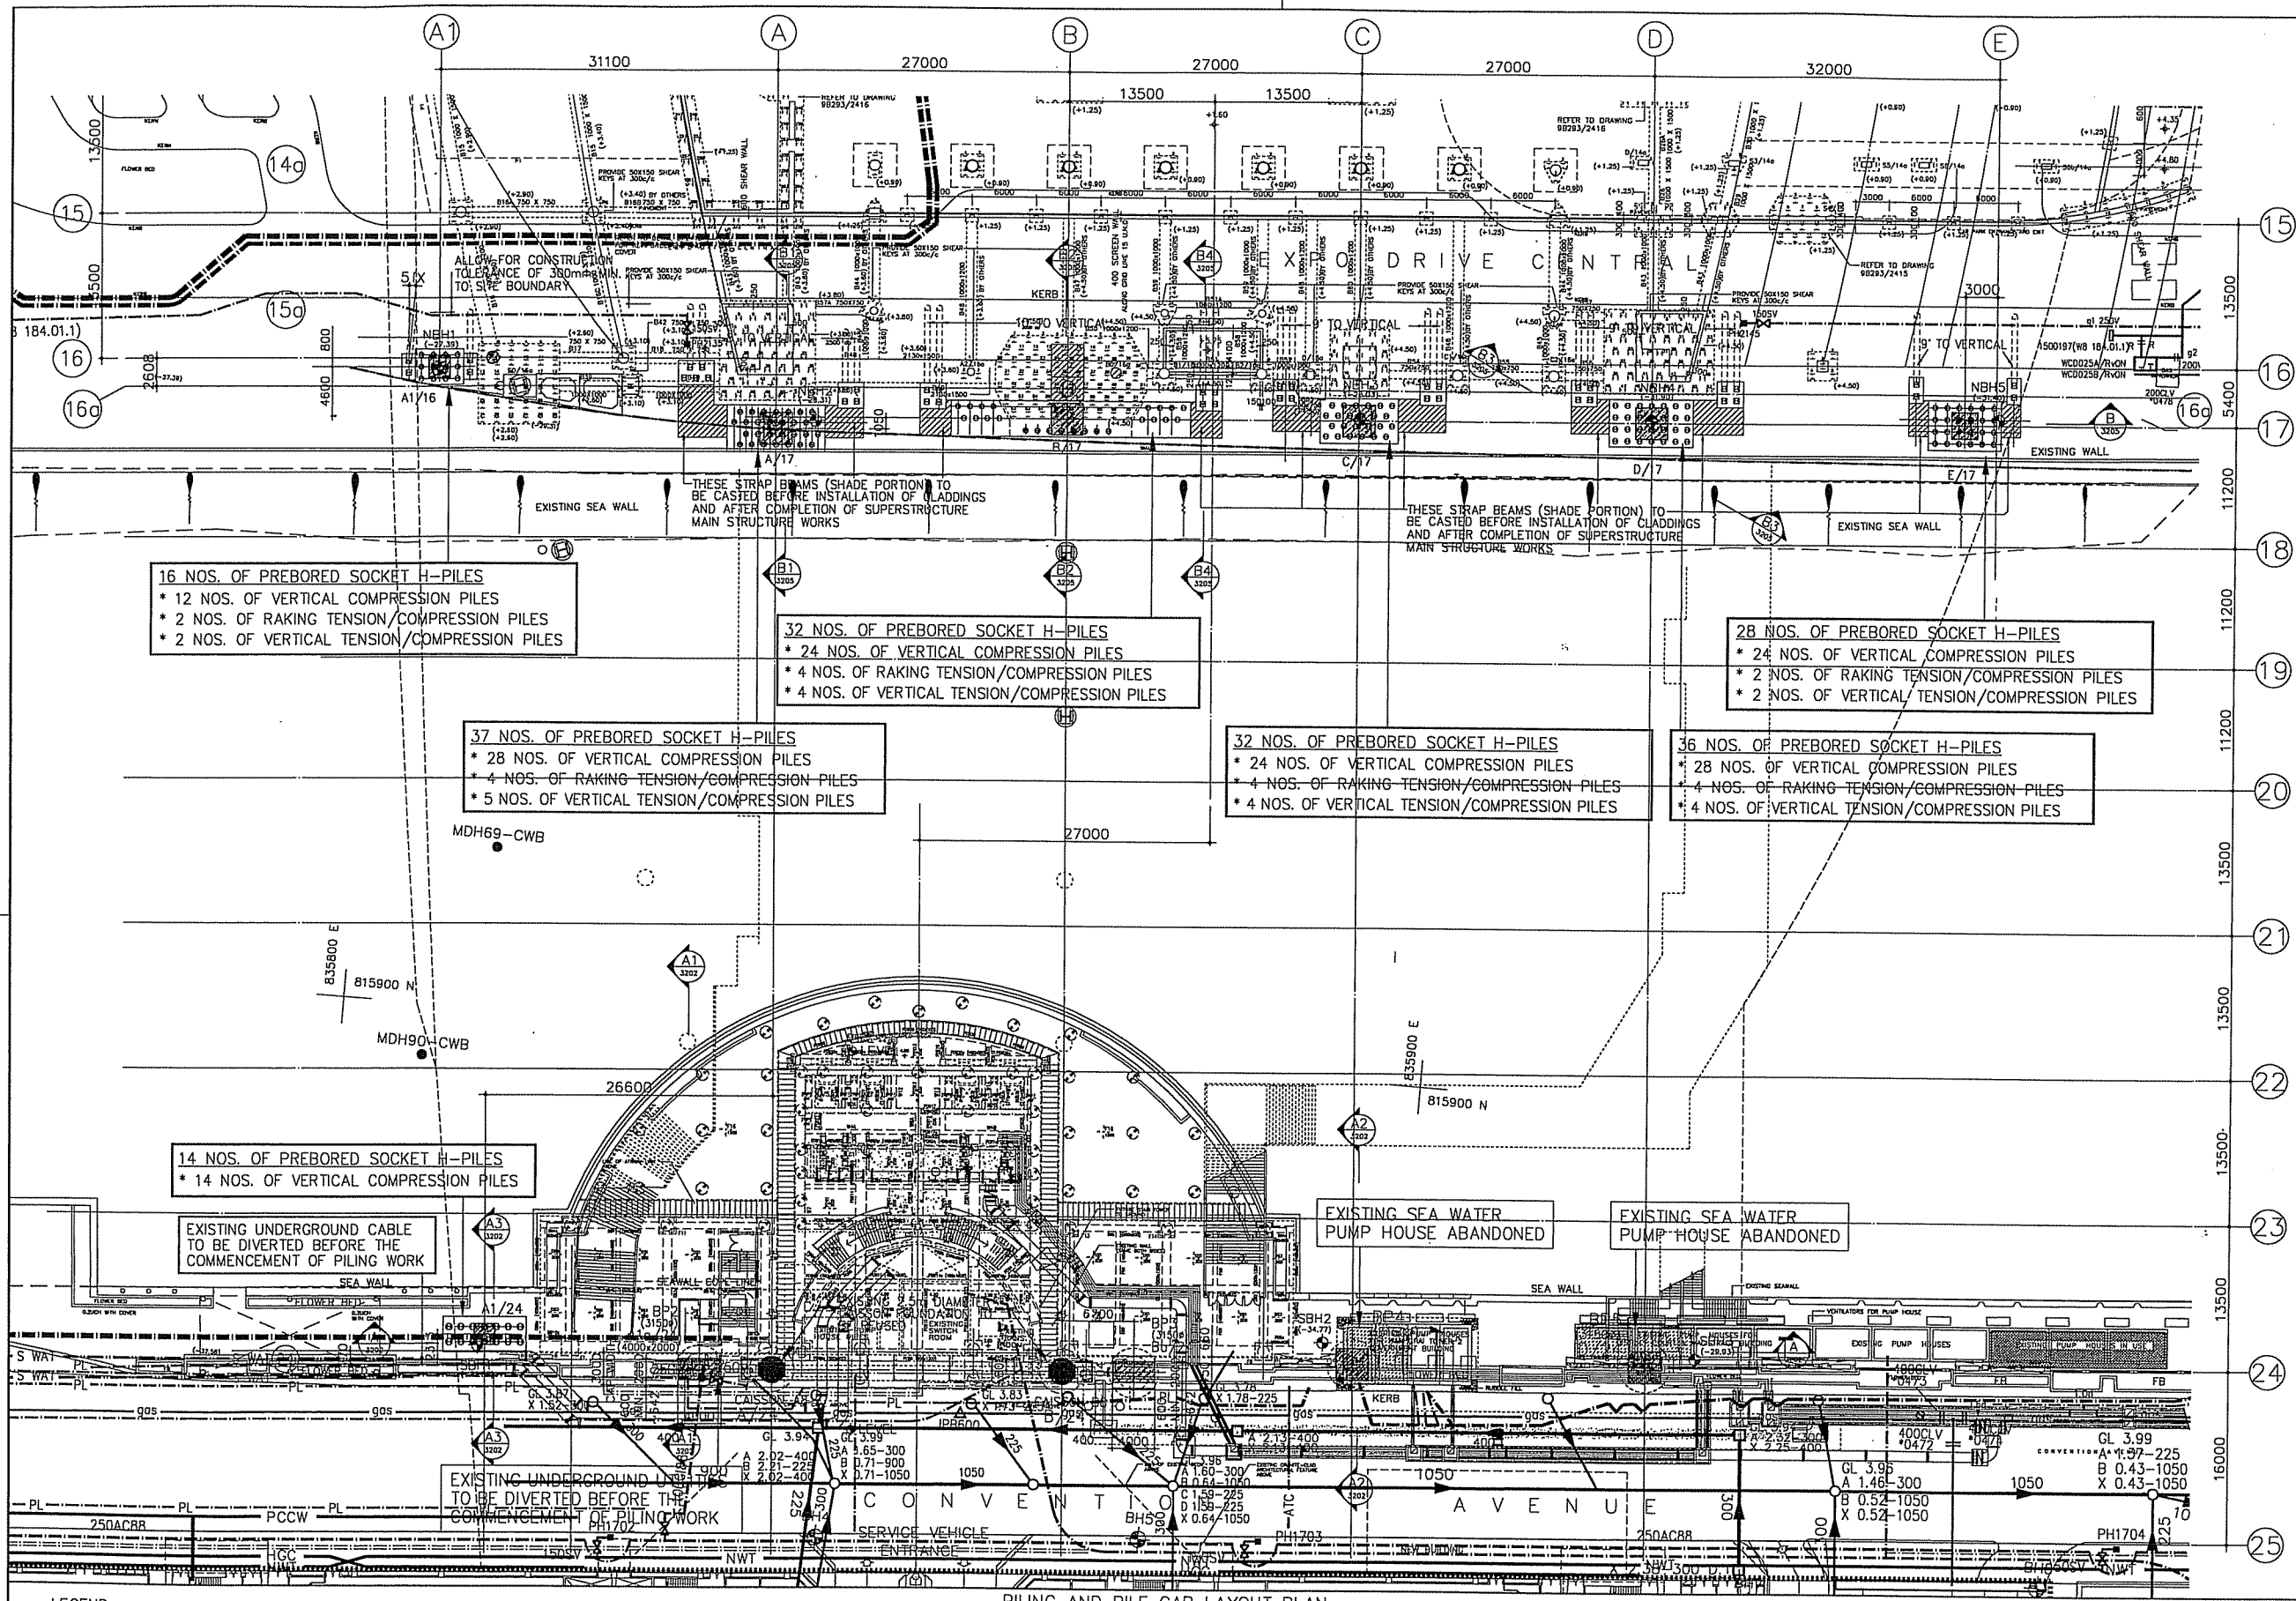


Annex B

Location of Construction
Activities during the
Reporting Month



B.L.D. REF		
F.S.D. REF		
REVISIONS		
NUMBER	DESCRIPTION	DATE
-	FOR SUBMISSION	9-6-06
A	PIILING FOR COLUMNS A1/24, A16/24, A/24, B/24 & B2/24 REVISED.	20-7-06
	FOR AMENDMENT SUBMISSION	21-7-06
B	PIILING FOR COLUMNS A1/16, A/17, B/17, C/17, D/17 & E/17 REVISED.	25-7-06
	FOR AMENDMENT SUBMISSION	26-7-06
C	REVISE DETAILS FOR BP4, BP5	31-7-06
	FOR AMENDMENT SUBMISSION (MTR)	3-8-06
D	REVISE DETAILS FOR A1/16, A/17, B/17, C/17, D/17 & E/17	4-8-06
	REPLACE SUBMISSION AT 26-7-06	4-8-06
E	FOR SUBMISSION TO CEDD	10-8-06
F	COLUMN A/17 LOCATION REVISED.	18-8-06

AMENDED PLAN

CLIENT	 香港貿易發展局 Hong Kong Trade Development Council	
MAIN CONTRACTOR	 Hip Hing - Ngo Kee Joint Venture	
ARCHITECT	 WONG & OUYANG (HK) LTD ARCHITECTS AND ENGINEERS	
STRUCTURAL ENGINEER	 WONG & OUYANG (CIVIL) STRUCTURAL ENGINEERING LTD.	
BUILDING SERVICES ENGINEER	 WONG & OUYANG (BUILDING SERVICES) LTD	
PROJECT	HONG KONG CONVENTION & EXHIBITION CENTRE EXPANSION PROJECT	
DRAWING TITLE	PILING AND PILE CAP LAYOUT PLAN (PREBORED H-PILE AND BORED PILE	
DESIGNER'S SIGNATURE FOR SUBMISSION		
SIGN	DATE	
INDEPENDENT DESIGN CHECKER'S SIGNATURE FOR SUBMISSION		
SIGN	DATE	
DRAWN BY	SIZE	DATE 24-2-06
ENTERED BY	CHK/PAX	PLOT DATE 26-7-06
CHECKED BY	LW	DATE 26-7-06
SCALE	1:300	PRINT DATE 26-7-06
JOB NUMBER	DRAWING NUMBER	REVISION
2119	3201	F
DO NOT SCALE OFF DRAWING. THIS DRAWING IS NOT FOR CONSTRUCTION PURPOSES UNLESS EXPRESSLY STATED. ALL RIGHTS RESERVED AND REPRODUCTION IN ANY FORM MUST BE APPROVED BY WONG & OUYANG (HK) LTD.		

PROGRESS PRINT


1 Progress Summary

Item	Description	Location
3.2	Preparation work for demolition	Grid 16 level 2-7
3.4	Mobilization for Prebored H piles.	G/F North Side G/F South Side
3.5	Prebored H piles had been commenced on 8 Aug 2006.	(E/17) (A/17) (A1/16) (A1/24) (B/17) (C/17)
3.7	Demolition of abandoned water pump room	G/F South side
3.8	Mobilization of percussion drill for bored pile had been commenced	G/F South Side
3.9	Mini Piles for marine platform	G/F South Side
3.10	Internal Hoarding erection for demolition works	Lv2, 3,5&7
3.11	Preparation work for dismantling of curtain wall	Level 2-7 Grid 16
3.12	E&M diversion at Grid 16	Level 1

Annex C

Project Organisation

Project Organization (with contact details)

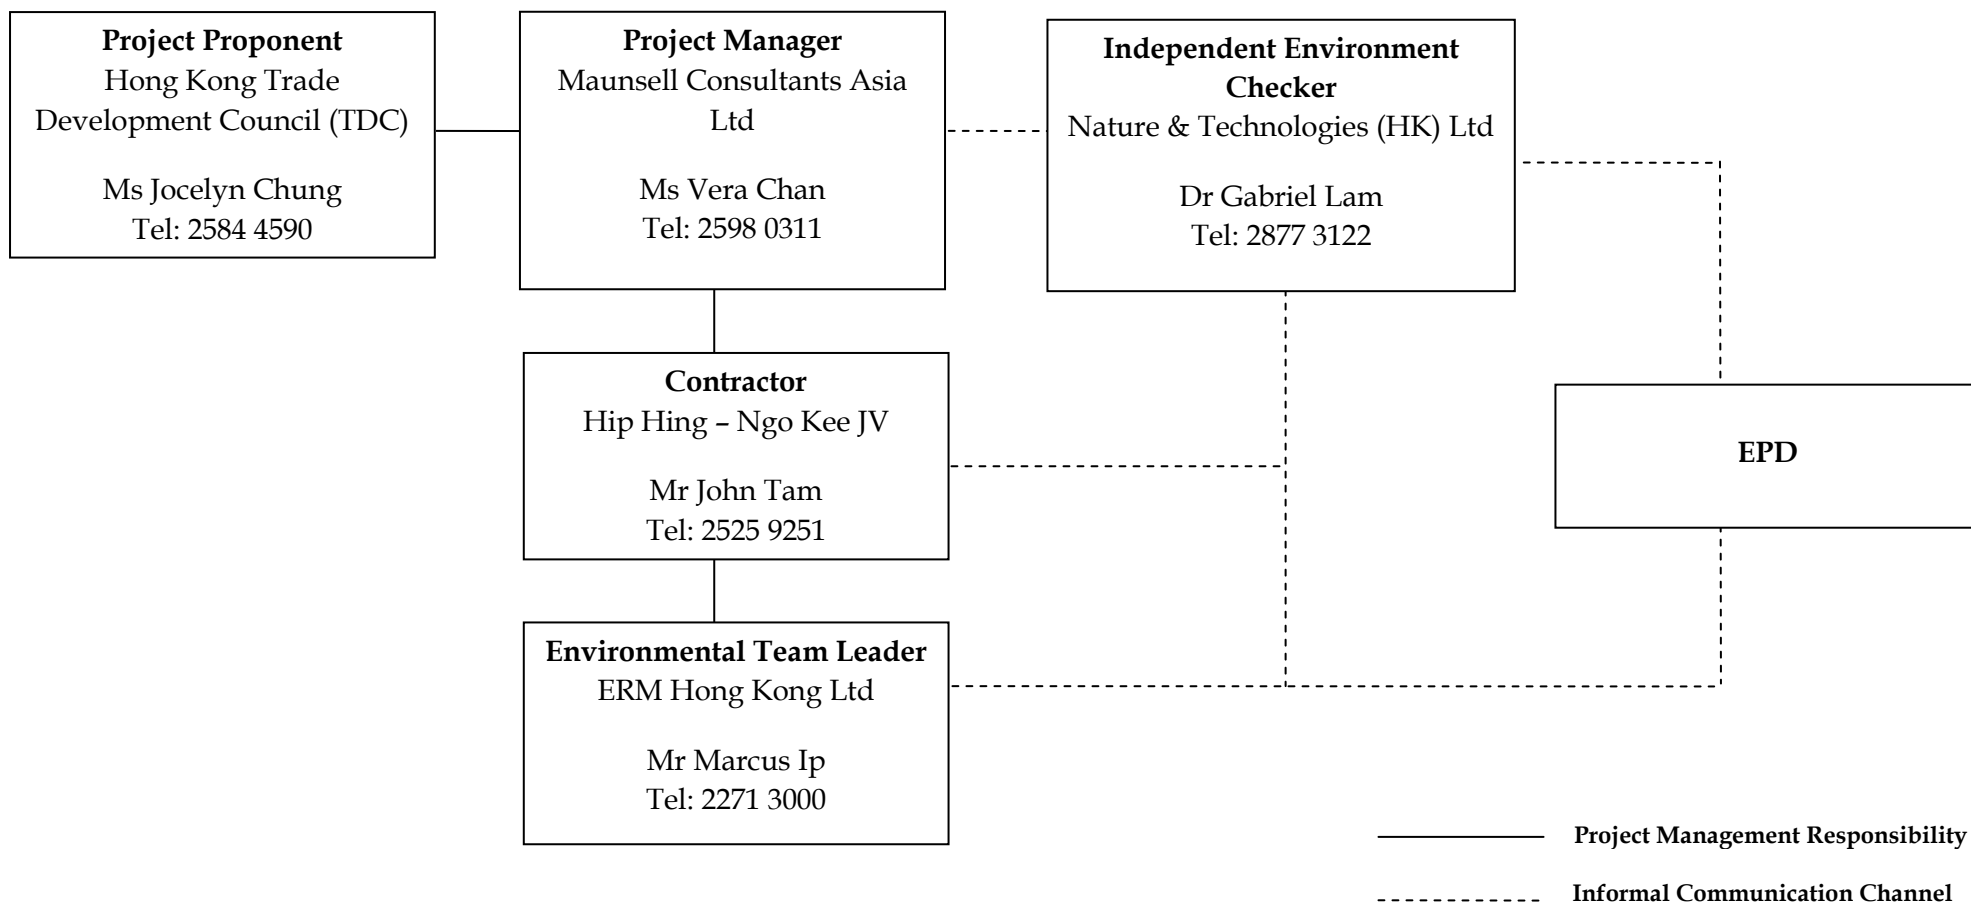

Annex D

Locations of Air and Water Quality Monitoring Stations

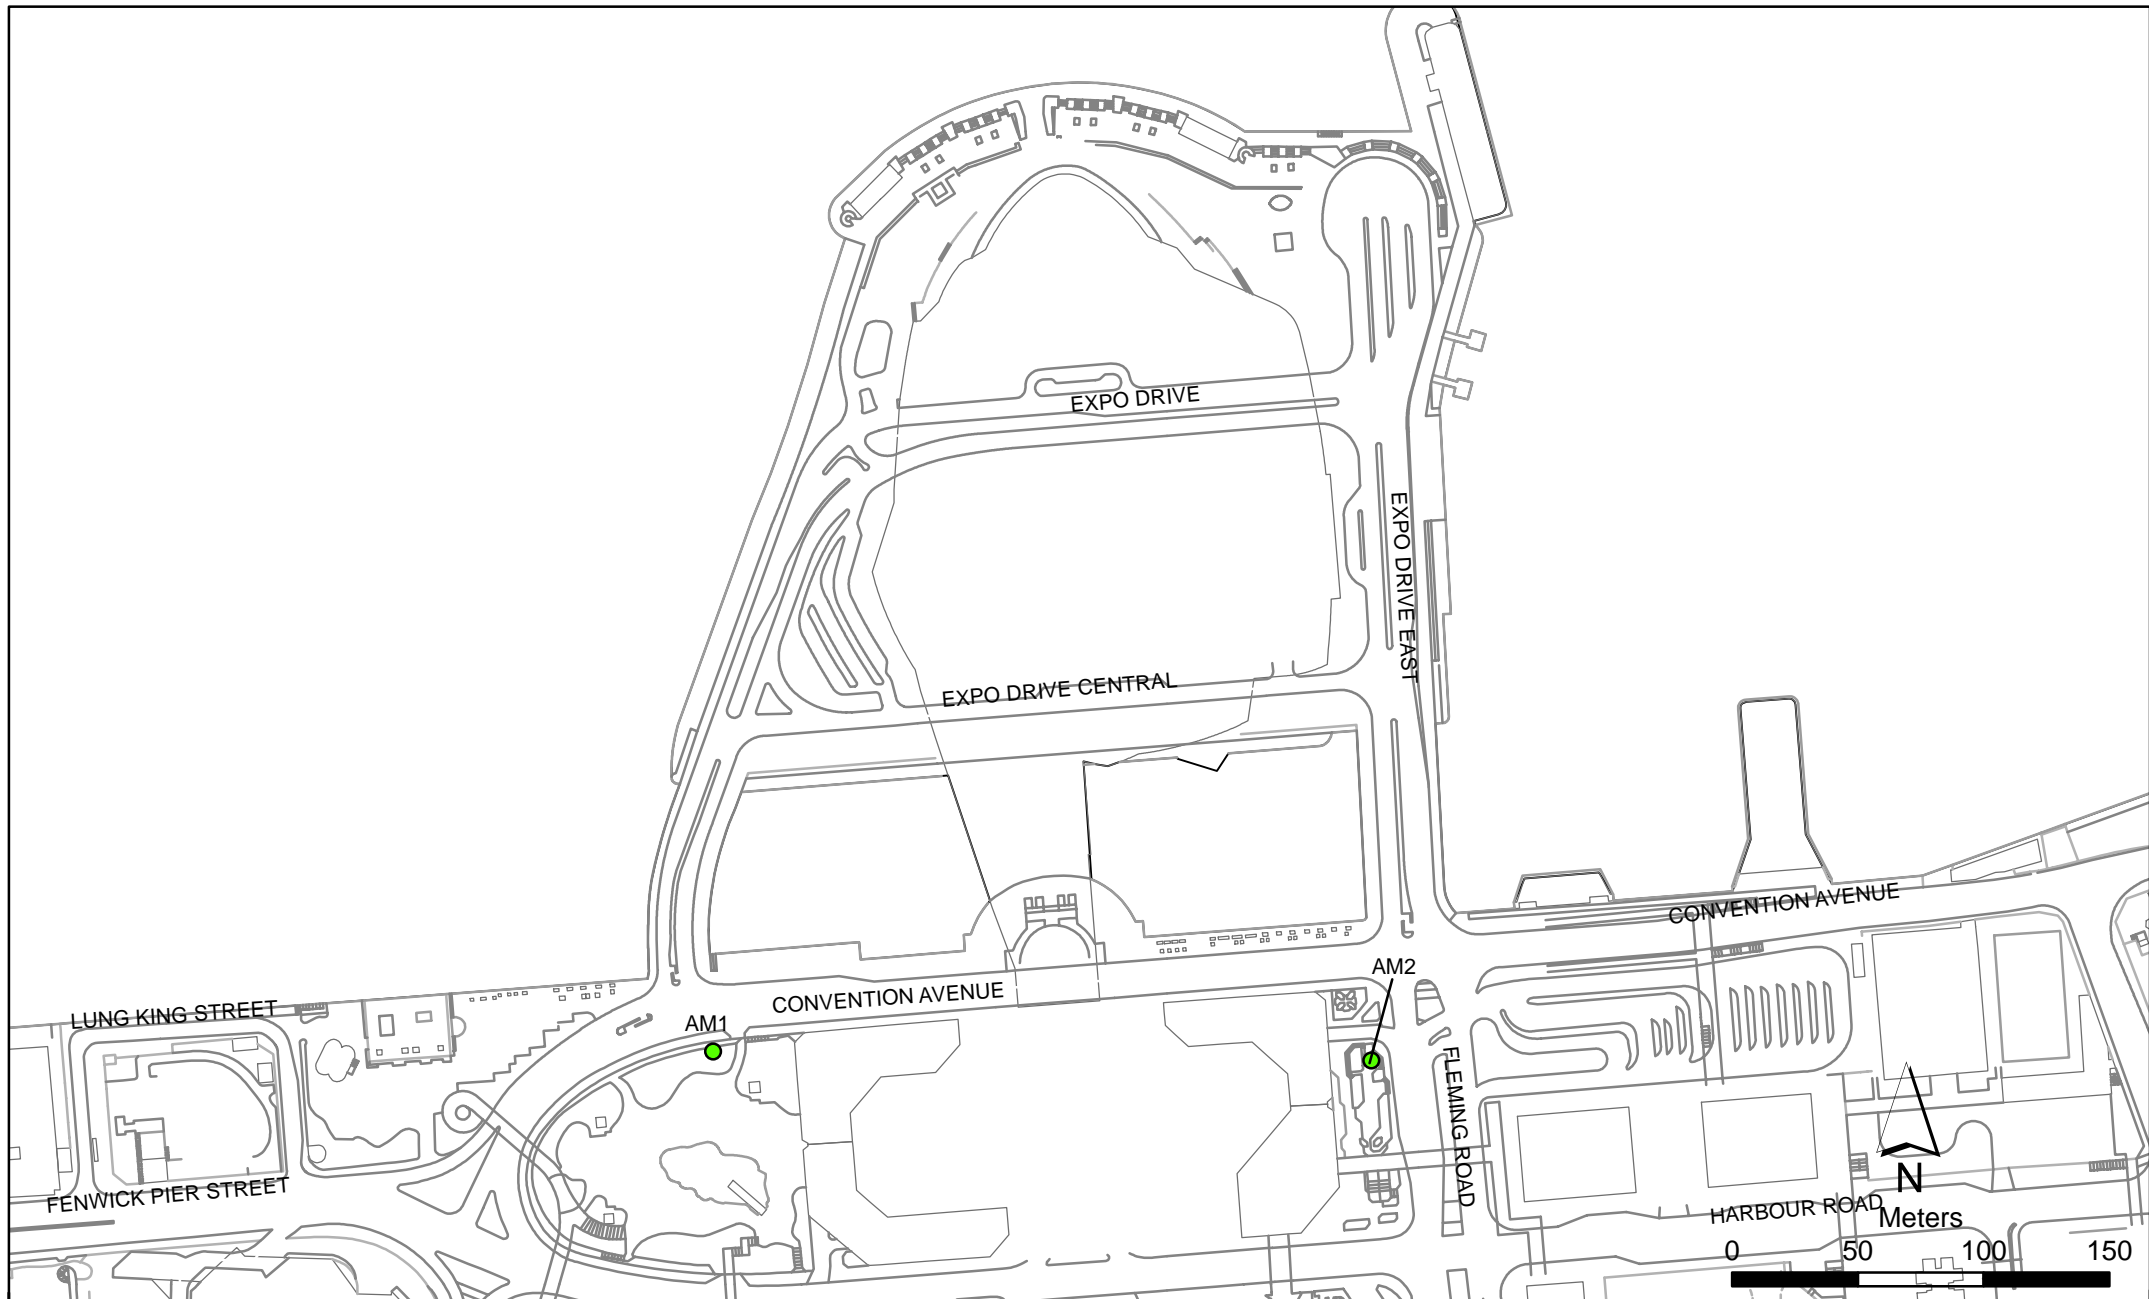


Figure D1

Air Quality Monitoring Station

File: 0050690_2.mxd
Date: 08/09/2006

Environmental
Resources
Management



Monitoring Station	Description	Easting	Northing
3	Hong Kong Convention and Exhibition Centre Phase I Cooling Water Intake	835852.3	815907.0
4	Wan Chai Tower/Revenue Tower/Immigration Towe Cooling Water Intake	835944.1	815885.0
5	Great Eagle Centre/China Resources Building Cooling Water Intake	835963.4	815886.5


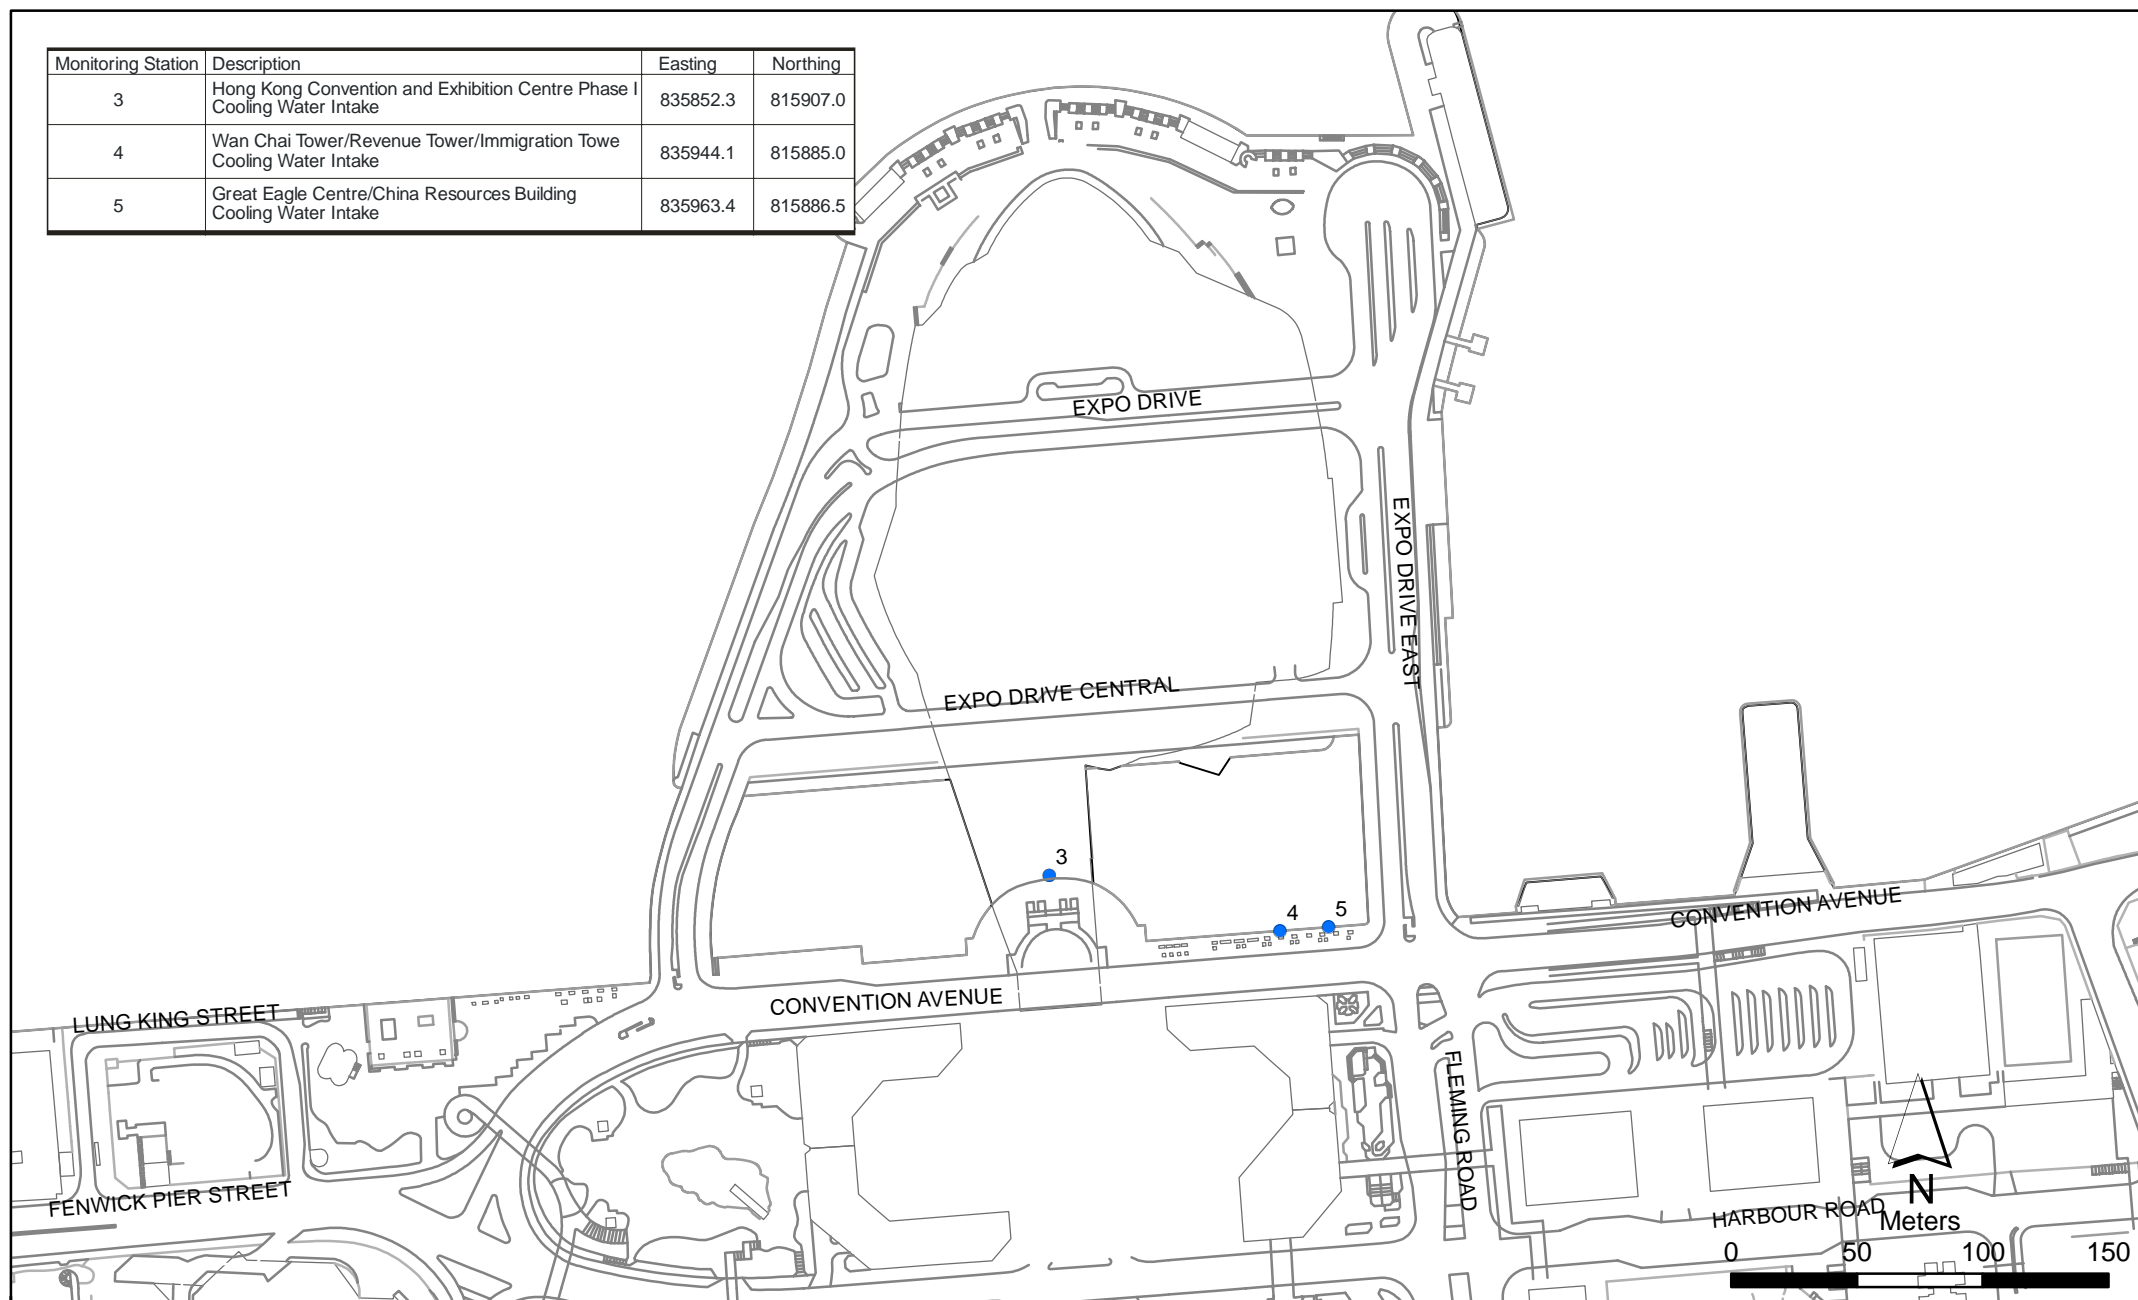


Figure D2


Marine Water Quality Monitoring Station



Air Quality Monitoring Station (AM1)

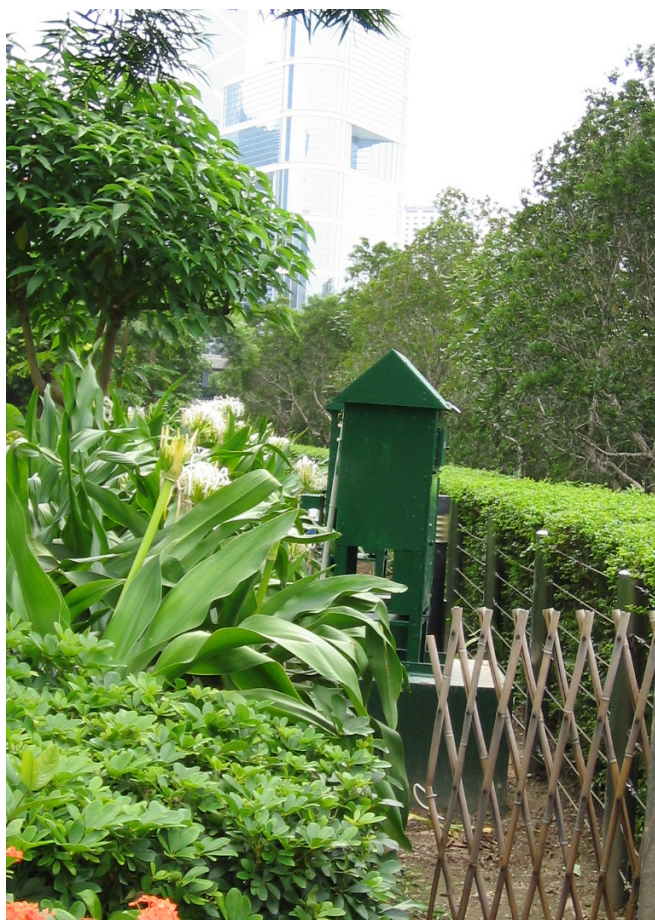

Air Quality Monitoring Station (AM2)

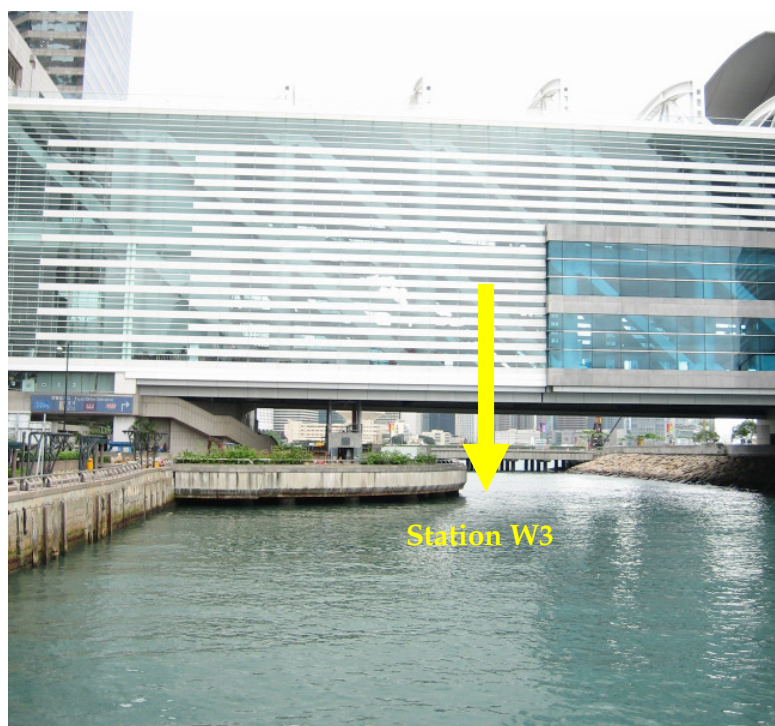

Water Quality Monitoring Location – Station W3



Water Quality Monitoring Location – Stations W4 and W5

Annex E

Monitoring Schedule from September to December 2006

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Air Quality Monitoring Schedule - September 2006

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					01-Sep	02-Sep
03-Sep	04-Sep	05-Sep	06-Sep	07-Sep	08-Sep	09-Sep
		Air Monitoring				
10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep
	Air Monitoring					Air Monitoring
17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep
					Air Monitoring	
24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep
				Air Monitoring		

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Air Quality Monitoring Schedule - October 2006

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
01-Oct	02-Oct	03-Oct	04-Oct	05-Oct	06-Oct	07-Oct
			Air Monitoring			
08-Oct	09-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct
		Air Monitoring				
15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct
	Air Monitoring					Air Monitoring
22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct	28-Oct
					Air Monitoring	
29-Oct	30-Oct	31-Oct				

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Air Quality Monitoring Schedule - November 2006

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			01-Nov	02-Nov	03-Nov	04-Nov
				Air Monitoring		
05-Nov	06-Nov	07-Nov	08-Nov	09-Nov	10-Nov	11-Nov
			Air Monitoring			
12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov	18-Nov
		Air Monitoring				
19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov
	Air Monitoring					Air Monitoring
26-Nov	27-Nov	28-Nov	29-Nov	30-Nov		

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Air Quality Monitoring Schedule - December 2006

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					01-Dec	02-Dec
					Air Monitoring	
03-Dec	04-Dec	05-Dec	06-Dec	07-Dec	08-Dec	09-Dec
				Air Monitoring		
10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec
			Air Monitoring			
17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec
		Air Monitoring				Air Monitoring
24-Dec	25-Dec	26-Dec	27-Dec	28-Dec	29-Dec	30-Dec
					Air Monitoring	
31-Dec						

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Water Quality Monitoring Schedule - October 2006


Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
01-Oct	02-Oct	03-Oct	04-Oct	05-Oct	06-Oct	07-Oct
08-Oct	09-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct
15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct
		Mid-Ebb 09:18 Mid-Flood 16:40		Mid-Ebb 10:46 Mid-Flood 17:13		Mid-Ebb 11:53 Mid-Flood 17:46
22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct	28-Oct
		Mid-Flood 13:25 Mid-Ebb 18:30		Mid-Flood 09:15 Proposed 18:00 Mid-Ebb 02:17 (out of piling hour)		Proposed 09:00 Mid-Flood 15:30 Mid-Ebb 04:14 (out of piling hour)
29-Oct	30-Oct	31-Oct				
		Mid-Ebb 09:00 Mid-Flood 15:19				

Hong Kong Convention and Exhibition Centre, Atrium Link Extension
Water Quality Monitoring Schedule - Nov 2006

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			01-Nov	02-Nov	03-Nov	04-Nov
				Mid-Ebb 09:20 Mid-Flood 16:13		Mid-Ebb 11:04 Mid-Flood 17:10
05-Nov	06-Nov	07-Nov	08-Nov	09-Nov	10-Nov	11-Nov
		Proposed 13:00 Mid-Flood 18:42 Mid-Ebb 01:36 (out of piling hour)		Mid-Flood 09:46 Proposed 12:30 Mid-Ebb 03:15 (out of piling hour)		Proposed 08:30 Mid-Flood 16:29 Mid-Ebb - (out of piling hour)
12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov	18-Nov
		Mid-Ebb 09:00 Mid-Flood 15:17		Mid-Ebb 09:18 Mid-Flood 15:55		Mid-Ebb 10:43 Mid-Flood 16:28
19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov
		Proposed 12:30 Mid-Flood 17:23 Mid-Ebb 00:21 (out of piling hour)		Proposed 13:00 Mid-Flood 18:04 Mid-Ebb 01:26 (out of piling hour)		Proposed 16:30 Mid-Flood 19:10 Mid-Ebb 02:59 (out of piling hour)
26-Nov	27-Nov	28-Nov	29-Nov	30-Nov		
		Proposed 09:00 Mid-Flood 13:25 Mid-Ebb 05:12 out of piling hour		Mid-Ebb 08:15 Mid-Flood 14:43		

Annex F

Calibration Reports for HVS



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etf@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com


TEST REPORT

Calibration Report
of
High Volume Air Sampler

Manufacturer : Graseby GMW Date of Calibration : 28 August 2006
Serial No. : 9864 (ET / EA / 003 / 19) Calibration Due Date : 27 October 2006
Method : Based on Operations Manual for the 5-point calibration using standard calibration kit manufactured by Tisch TE-5025 A

Results	Flow recorder reading (cfm)	53	47	41	33	25
	Qstd (Actual flow rate, m ³ /min)	1.67	1.49	1.30	1.02	0.81
	Pressure : 758.31 mm Hg	Temp. : 303 K				

Sampler 9864 Calibration Curve
Site: Wan Chai (AM1-1hr.)
Date of Calibration: 28 August 2006

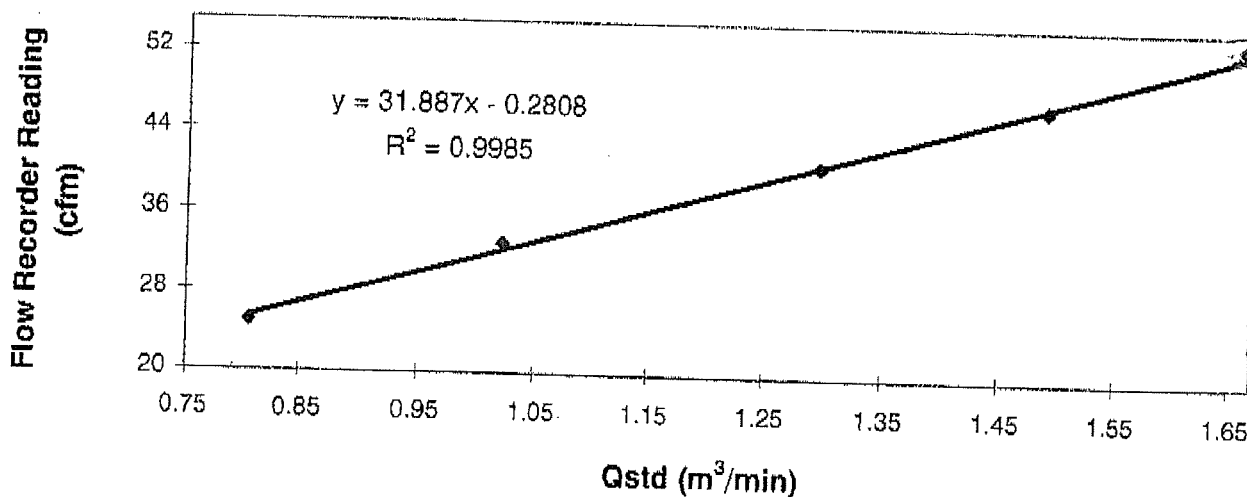


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by : Mak Kei Wai
Mak Kei Wai
(Technician)

Approved by : H. T. Chow
H. T. Chow
(Asst. Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Foton, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com


TEST REPORT

**Calibration Report
of
High Volume Air Sampler**

Manufacturer : Graseby GMW Date of Calibration : 28 August 2006
Serial No. : 9795 (ET / EA / 003 / 18) Calibration Due Date : 27 October 2006
Method : Based on Operations Manual for the 5-point calibration using standard calibration kit manufactured by Tisch TE-5025 A

Results	Flow recorder reading (cfm)	43	38	31	22	12
	Qstd (Actual flow rate, m ³ /min)	1.64	1.45	1.27	1.01	0.81
	Pressure : 758.31 mm Hg	Temp. : 302 K				

Sampler 9795 Calibration Curve
Site: Wan Chai (AM2-24hr.)
Date of Calibration: 28 August 2006

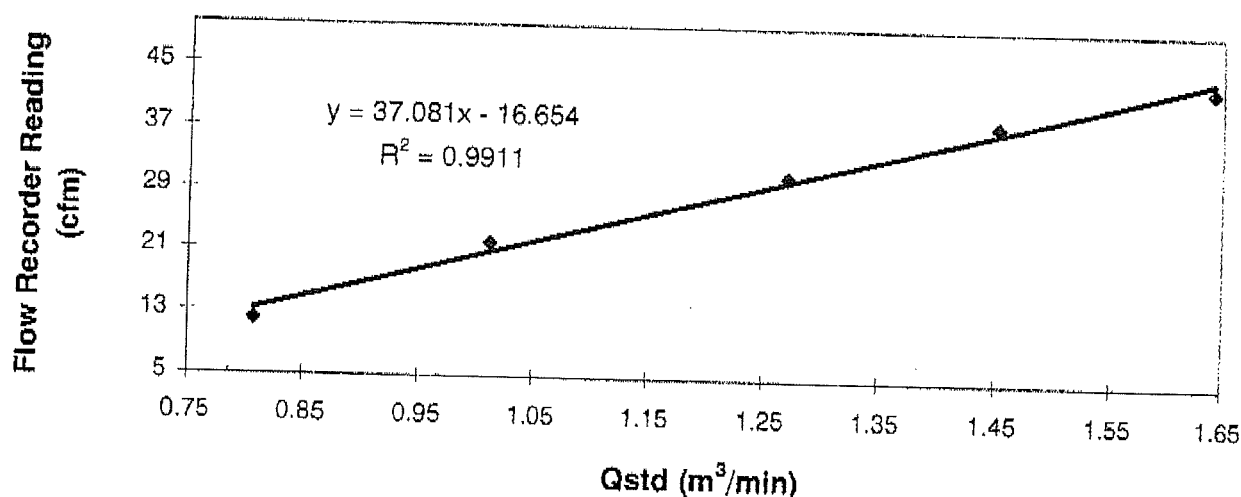

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / ~~unacceptable~~ * for use.

Calibrated by : Mak Kei Wai
Mak Kei Wai
(Technician)

Approved by : H. T. Chow
H. T. Chow
(Asst. Environmental Officer)

Annex G

Event Action Plans for Air and Water Quality Monitoring

Table G1 Event Action Plans for Air Quality

Event Action Level	Action			
	ET	Contractor	ER	IEC
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source 2. Notify IEC, ER and Contractor within 1 working day after receiving the laboratory results. 3. Conduct additional monitoring to investigate the causes. 4. Report the investigation results and if exceedance is due to contractor's construction works to the IEC, ER and Contractor. 5. Increase monitoring frequency to once per 2 days for 24-hour TSP and daily for 1-hour TSP until exceedance stops if exceedances are considered related to contractor's construction works and report the results to IEC, ER and Contractor within 1 working day after receiving the laboratory results. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance and rectify any unacceptable practice. 2. Submit air mitigation proposal to IEC and ER for agreement within 3 working days if ET indicated that exceedance is related to the construction works 3. Implement agreed proposal within a time scale agreed with ER and IEC. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify Contractor. 3. Require Contractor to submit air mitigation proposal. 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Review monitoring data and investigation report submitted by ET. 2. Review Contractor's air mitigation proposal and advise the ER accordingly. 3. Supervise and confirm in writing the implementation of remedial measures within 2 working days after receipt of the mitigation proposal.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source 2. Notify EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results 3. Conduct additional monitoring to investigate the causes. 4. Report the investigation results and if exceedances are due to contractor's construction works to EPD, IEC, ER and Contractor within 3 working days after additional monitoring. 5. Increase monitoring frequency to daily for 24-hour TSP and 1-hour TSP if exceedances are considered related to contractor's construction works until exceedance stops, and report the results to EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results. 6. If exceedances continue after 1-week monitoring events, request ER to arrange meeting with ER, IEC and contractor to discuss remedial actions. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance and rectify any unacceptable practice 2. In consultation with the IEC, submit air mitigation proposal to IEC and ER for agreement within 3 working days of notification if ET indicated that exceedances are related to construction works 3. Implement agreed proposal within a time scale agreed with ER and IEC. 4. Amend working methods if appropriate. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify Contractor. 3. Require Contractor to submit air mitigation proposal. 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Review monitoring data and investigation report submitted by ET. 2. Discuss amongst ER, ET and Contractor in order to formulate air mitigation proposal. 3. Review Contractor's air mitigation proposal and advise the ER accordingly. 4. Supervise and confirm in writing the implementation of remedial measures within 2 working days after receipt of the mitigation proposal.

Event Limit Level	Action			
	ET	Contractor	ER	IEC
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source 2. Notify EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results 3. Conduct additional monitoring to investigate the causes. 4. Report the investigation results and if exceedances are due to contractor's construction works to EPD, IEC, ER and Contractor within 3 working days after additional monitoring. 5. Increase monitoring frequency to daily if exceedances are considered related to contractor's construction works until exceedance stops, and report the results to EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance and rectify any unacceptable practice 2. In consultation with the IEC, submit air mitigation proposal to IEC and ER for agreement within 3 working days of notification if ET indicated that exceedances are related to construction works 3. Implement agreed proposal within a time scale agreed with ER and IEC. 4. Amend working methods if appropriate. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify Contractor. 3. Require Contractor to submit air mitigation proposal. 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Review monitoring data and investigation report submitted by ET. 2. Discuss amongst ER, ET and Contractor in order to formulate air mitigation proposal. 3. Review Contractor's air mitigation proposal and advise the ER accordingly. 4. Supervise and confirm in writing the implementation of remedial measures within 2 working days after receipt of the mitigation proposal.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source 2. Notify EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results 3. Conduct additional monitoring to investigate the causes. 4. Report the investigation results and if exceedances are due to contractor's construction works to EPD, IEC, ER and Contractor within 3 working days after additional monitoring. 5. Increase monitoring frequency to daily if exceedances are considered related to contractor's construction works until exceedance stops, and report the results to EPD, IEC, ER and Contractor within 1 working day after receiving the laboratory results. 6. If exceedances continue after 2 consecutive monitoring events, request ER to arrange meeting with IEC and contractor to discuss remedial actions. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance and rectify any unacceptable practice 2. In consultation with the IEC, submit air mitigation proposal to IEC and ER for agreement within 3 working days of notification if ET indicated that exceedances are related to construction works 3. Implement agreed proposal within a time scale agreed with ER and IEC. 4. Amend working methods and proposal if appropriate. 5. Stop relevant portion(s) of works as required by ER, ET and IEC 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify Contractor. 3. Require Contractor to submit air mitigation proposal. 4. Ensure remedial measures are properly implemented. 5. If exceedances continue arrange meeting with Contractor, IEC and ET and to consider what portion(s) of works should be further mitigated or have to stop. 	<ol style="list-style-type: none"> 1. Review monitoring data and investigation report submitted by ET. 2. Discuss amongst ER, ET and Contractor in order to formulate air mitigation proposal. 3. Review Contractor's air mitigation proposal and advise the ER accordingly. 4. Supervise and confirm in writing the implementation of remedial measures within 2 working days after receipt of the mitigation proposal.

Table H2 Event Action Plans for Water Quality

Event	Action			
	ET	IC(E)	ER	Contractor
Action level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. (The above actions should be taken within 1 working day after the exceedance is identified) 7. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented. 3. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures. 7. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	<ol style="list-style-type: none"> 1. Identify source(s) of impact; 2. Inform IC(E) and Contractor; 3. Check monitoring data, all plant, equipment and Contractor's working methods; 4. Discuss mitigation measures with IC(E) and Contractor; 5. Ensure mitigation measures are implemented; 6. Prepare to increase the monitoring frequency to daily; 7. (The above actions should be taken within 1 working day after the exceedance is identified) 8. Repeat measurement on next working day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER within 3 working days; 6. Implement the agreed mitigation measures. 7. (The above actions should be taken within 1 working day after the exceedance is identified)

Event	Action			
	ET	IC(E)	ER	Contractor
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IC(E), contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E), ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level. 8. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with IC(E), ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures. 5. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET , IC(E) and ER and propose mitigation measures to IC(E) and ER within 3 working days; 6. Implement the agreed mitigation measures. 7. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive samplig days	<ol style="list-style-type: none"> 1. Identify source(s) of impact; 2. Inform IC(E), contractor and EPD; 3. Check monitoring data, all plant, equipment and Contractor's working methods; 4. Discuss mitigation measures with IC(E), ER and Contractor; 5. Ensure mitigation measures are implemented; 6. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. 7. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Discuss with IC(E), ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. 6. (The above actions should be taken within 1 working day after the exceedance is identified) 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET , IC(E) and ER and propose mitigation measures to IC(E) and ER within 3working days; 6. Implement the agreed mitigation measures; 7. As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. 8. (The above actions should be taken within 1 working day after the exceedance is identified)

Annex H

Summary of Implementation Status

Annex H - Summary of Environmental Protection / Mitigation Activities

Environmental Permit No. EP-239/2006

EP Condition Ref	Submission	Action Required by the Permit Holder	Implementation Status
Measures for Mitigating Water Quality Impact			
2.4	Method statement on silt screens for seawater intakes (including design and maintenance requirements)	2 weeks before commencement of marine pile installation works	Method statement was submitted to the EPD on 21/6/06. Method statement (Revision A) was submitted to the EPD on 29/9/06.
2.5	Method statement on silt curtain system for marine piling works (including design and maintenance requirements)	2 weeks before commencement of marine pile installation works	Method statement was submitted to the EPD on 15/9/06
2.8	Design drawings specifying pile dimension and layout	2 weeks before commencement of marine pile installation works	Design drawing was submitted to the EPD on 22/8/06
Measures for Mitigating Air Quality Impact			
2.9	Design drawings of ventilation facility for fresh air intakes (req'd only before operation of Project)	2 weeks before commencement of installation of ventilation facility	---
Measures for Mitigating Landscape and Visual Impact			
2.10	Implementation programme for landscape and visual mitigation measures (for both construction and operational phases of Project)	Within 6 months after commencement of construction of Project	---
2.10	Details of each landscape and visual mitigation measures package (incl plans)	2 weeks before implementation of a particular mitigation package	---
3.2	Baseline Monitoring Report	One week before the commencement of construction	Report was submitted to the EPD on 24 Jul 06 and comments from the EPD was received on 3 Aug 06. Revised report was submitted to EPD on 17 Aug 06 and no further comments received.

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>			
Air Quality	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. A number of practical measures are listed below:</p> <ul style="list-style-type: none"> • skip hoist for material transport should be totally enclosed by impervious sheeting; • every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site; • the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; • where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit; • every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides; • all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet; • the height from which excavated materials dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading; • the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle; and • instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. 	Work site / during construction	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Air Quality	Some fresh air intakes of the Hong Kong Convention and Exhibition Centre Phase I, Renaissance Harbour View Hotel and Grand Hyatt Hotel (ASRs A4, A5 and A6) should be re-diverted to the new air vent shaft provided for Atrium Link Extension where fresh air intake located at +55.8mPD.	Location of ASRs A4, A5 & A6 / Design & Operation Stage (Long-term and Interim Scenario)	NA
Air Quality	Monitoring of NO2 concentration underneath the Atrium Link Extension should be conducted.	Underneath the deckover / The first six months upon completion of the ALE.	NA
<i>Construction Phase</i>			
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program; silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program; mobile plant, if any, should be sited as far from NSRs as possible; machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities; <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	Construction work areas / Construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Noise	<p>The following noise reduction measures should be considered as far as practicable during detailed design:</p> <ul style="list-style-type: none"> • choose quieter plant such as those which have been effectively silenced; • include noise levels specification when ordering new plant; • locate fixed plant away from any NSRs as far as practicable; • locate fixed plant in plant rooms with thick walls or specially designed enclosure; • locate noisy machines in basement or a completely separate building; and • develop and implement a regularly scheduled plant maintenance programme in order to maintain controlled level of noise. 	Plant Room / Design and Operation Stage	NA
<i>Construction Phase</i>			
Water Quality	There should be no permanent structure in the water channel.	At the ALE sea channel / during operational phase	√
Water Quality	No dredging and no reclamation should be carried out for the Project.	At work sites / during construction phase	√
Water Quality	The marine pile layout as shown in Figure 2.6 of the EIA report should be adopted. No more than approximately 80 numbers of temporary marine piles should be installed in the ALE sea channel during the construction phase. The dimension of each temporary marine pile should be 800mm nominal diameter. These piles should be driven into position and internal space should not be excavated, i.e. left as soil. No dredging or soil /sediment excavation should be carried out. Marine piles would be removed by reverse driving.	At work sites / during construction phase	NA
Water Quality	Two layers of silt curtain should be installed around each of the marine piling and pile extraction locations. The proposed silt curtain should be extended to seabed with sinker blocks and regularly inspected and maintained to ensure it is serviceable.	At marine work sites and nearby seawater intakes / during marine piling and marine pile extraction	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	All marine works should be carried out in a controlled manner such that release of sediments into the marine environment would be minimized. All wastewater generated from the piling activities should be collected and be treated before controlled discharge. Spoil should also be properly collected for proper disposal.		
Water Quality	In view of the close vicinity of the seawater intakes to the work site, silt screens are recommended to be deployed at the seawater intakes shown in Figure 5.2 of the EIA report during the whole construction period. Silt screens to be provided at seawater intakes should be regularly checked and maintained to ensure that they are serviceable. Refuse collection vessel should be mobilized on a need basis to collect any floating refuse lost from/ trapped at the work site during the construction period.	At seawater intakes / during the whole construction period	√
Water Quality	Surface run-off from construction sites should be discharged into storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sedimentation basins. Channels or earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels at site boundaries should be provided where necessary to intercept storm runoff from outside the site so that it will not wash across the site. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks. Silt removal facilities, channels and manholes should be maintained and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. Any practical options for the diversion and re-alignment of drainage should comply with both engineering and environmental requirements in order to ensure adequate hydraulic capacity of all drains. Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the nearby saltwater intakes.	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>There is a need to apply to EPD for a discharge license for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge license. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Reuse and recycling of the treated effluent can minimize water consumption and reduce the effluent discharge volume. The beneficial uses of the treated effluent may include dust suppression, wheel washing and general cleaning. It is anticipated that only a small quantity of wastewater would be generated from the works areas. Any effluent discharge from the construction activities should be diverted away from the sea channel so as to avoid adverse water quality impact. Construction works should be programmed to minimize excavation works in rainy seasons (April to September). If excavation in soil could not be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion, temporary exposed slope surfaces should be covered e.g. by tarpaulin, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place to ensure that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm.</p>	Works areas / construction period	√
Water Quality	<p>Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.</p> <p>Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations</p>	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>should be discharged into storm drains via silt removal facilities.</p> <p>Open stockpiles of construction materials (e.g. aggregates, sand and fill material) on sites should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.</p> <p>Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.</p>		
Water Quality	Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	Works areas / construction period	√
Water Quality	Under normal circumstances, groundwater pumped out of wells, etc. for the lowering of ground water level in basement or foundation construction should be discharged into storm drains after the removal of silt in silt removal facilities.	Works areas / construction period	√
Water Quality	Water used in ground boring and drilling or rock /soil anchoring should as far as practicable be re-circulated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	Works areas / construction period	√
Water Quality	Wastewater generated from the washing down of mixing trucks and drum mixers and similar equipment should whenever practicable be recycled. The discharge of wastewater should be kept to a minimum.	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>To prevent pollution from wastewater overflow, the pump sump of any water recycling system should be provided with an on-line standby pump of adequate capacity and with automatic alternating devices.</p> <p>Under normal circumstances, surplus wastewater may be discharged into foul sewers after treatment in silt removal and pH adjustment facilities (to within the pH range of 6 to 10). Disposal of wastewater into storm drains will require more elaborate treatment.</p>		
Water Quality	<p>All vehicles and plant should be cleaned before they leave a construction site to ensure no earth, mud, debris and the like is deposited by them on roads.</p> <p>A wheel washing bay should be provided at every site exit if practicable and wash-water should have sand and silt settled out or removed before discharging into storm drains. The section of construction road between the wheel washing bay and the public road should be paved with backfall to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.</p>	Works areas / construction period	√
Water Quality	<p>Bentonite slurries used in diaphragm wall and bore-pile construction should be reconditioned and reused wherever practicable. If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis.</p> <p>If the used bentonite slurry is intended to be disposed of through the public drainage system, it should be treated to the respective effluent standards applicable to foul sewer, storm drains or the receiving waters as set out in the WPCO Technical Memorandum on Effluent Standards.</p>	Works areas / construction period	NA

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>Water used in water testing to check leakage of structures and pipes should be reused for other purposes as far as practicable. Surplus unpolluted water could be discharged into storm drains.</p> <p>Sterilization is commonly accomplished by chlorination. Specific advice from EPD should be sought during the design stage of the works with regard to the disposal of the sterilizing water. The sterilizing water should be reused wherever practicable.</p> <p>Discharge of sterilization effluent should be properly pre-treated for compliance with TM/WPCO requirements, such as but not limited to total residual chlorine.</p>	Works areas / construction period	
Water Quality	<p>Effluent discharges from building construction and other construction site activities are subject to WPCO control. Before commencing any demolition works, all sewer and drainage connections should be sealed to prevent building debris, soil, sand etc. from entering public sewers/drains.</p> <p>Wastewater generated from building construction activities including concreting, plastering, internal decoration, cleaning of works and similar activities should not be discharged into the stormwater drainage system. If the wastewater is to be discharged into foul sewers, it should undergo the removal of settleable solids in a silt removal facility, and pH adjustment as necessary.</p>	Works areas / construction period	√
Water Quality	<p>Acidic wastewater generated from acid cleaning, etching, pickling and similar activities should be neutralized to within the pH range of 6 to 10 before discharging into foul sewers. If there is no public foul sewer in the vicinity, the neutralized wastewater should be tinkered off site for disposal into foul sewers or treated to a standard acceptable to storm drains and the receiving waters.</p>	Works areas / construction period	NA
Water Quality	<p>Wastewater collected from canteen kitchens, including that from basins, sinks and floor drains, should be discharged into foul</p>	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>sewer via grease traps capable of providing at least 20 minutes retention during peak flow.</p> <p>Drainage serving an open oil filling point should be connected to storm drains via a petrol interceptors with peak storm bypass.</p> <p>Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance.</p>		
Water Quality	<p>It is recommended to provide sufficient chemical toilets in the works areas. The toilet facilities should be more than 30 m from the seafront or any watercourse. A licensed waste collector should be deployed to clean the chemical toilets on a regular basis.</p> <p>Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment. Regular environmental audit on the construction site can provide an effective control of any malpractices and can encourage continual improvement of environmental performance on site.</p>	Works areas / construction period	√
Water Quality	Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	Works areas / construction period	√
Water Quality	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p> <p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</p> <ul style="list-style-type: none"> • suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport; • chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and • storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 		
Water Quality	<p>To minimize the potential water quality impacts from the construction works located at or near the storm system or seafront, the following mitigation measures should be adopted:</p> <ul style="list-style-type: none"> • the use of less or smaller construction plants may be specified to reduce the disturbance to the seabed; • temporary sewerage system should be designed to prevent wastewater from entering the storm system and sea; • temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works; • stockpiling of construction materials and dusty materials should be covered and located away from any water courses; • construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers; • construction activities, which generate large amount of 	Works areas / construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>wastewater, should be carried out in a distance away from the waterfront, where practicable;</p> <ul style="list-style-type: none"> • mitigation measures to control site runoff from entering the nearby water environment should be implemented to minimize water quality impacts. Surface channels should be provided along the edge of the waterfront within the work sites to intercept the runoff; • construction effluent, site run-off and sewage should be properly collected and/or treated; • proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert/sea; and • supervisory staff should be assigned to station on site to closely supervise and monitor the works. 		
Water Quality	If monitoring of the treated effluent quality from the Works Areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. The contractor should submit detailed monitoring programme to EPD for approval before commencement of the construction activities.	Works areas / construction period	√
Water Quality	Monitoring of the water quality at the seawater intakes inside the ALE sea channel should be conducted.	ALE sea channel / Before construction period and during installation and removal of temporary marine piles.	NA
Water Quality	All barges should be fitted with tight seals to their bottom opening to prevent leakage of materials. The decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard. Loading of barges should be controlled to prevent splashing of materials to the surrounding environment and barges should under no circumstances be filled to a level which would cause overflowing of material or sediment laden water during loading and transportation. All barges should maintain adequate clearance between vessels and the seabed at all states of the tide and	Works areas / construction period	NA

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	should operate at a reduced speeds to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.		
Water Quality	Connection of sewage generated from the ALE will be connected to the existing public sewer. For handling, treatment and disposal of other operational stage effluent, the practices outlined in ProPECC PN 5/93 should be adopted where applicable. Consensus from DSD should be sought on technical details of the drainage and sewerage proposals.	Project site / design and construction period	NA
<i>Construction Phase</i>			
Waste	<p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> • nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all Wastes generated at the site; • training of site personnel in proper waste management and chemical handling procedures; • provision of sufficient waste disposal points and regular collection of waste; • appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; and • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. 	Work site / during the construction period	√
Waste	<p>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> • sorting of demolition debris and excavated materials from demolition works to recover reusable/ recyclable portions (ie soil, broken concrete, metal, etc); • segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or 	Work site / during the construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>recycling of materials and their proper disposal;</p> <ul style="list-style-type: none"> encourage collection of aluminum cans by individual collectors by providing separate labeled bins to enable this waste to be segregated from other general refuse generated by the work force; proper storage and site practices to minimize the potential for damage to contamination of construction materials; and plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste. 		
Waste	<p><u>General Refuse</u></p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.</p>	Work site / during the construction period	√
Waste	<p><u>Construction and Demolition Material</u></p> <ul style="list-style-type: none"> In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the C&D material from the following construction activities should be reused and recycled as far as possible to reduce the net amount of C&D material generated from the Project; a Waste Management Plan should be prepared in accordance with ETWB TCW No. 19/2005; a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed; in order to monitor the disposal of C&D and solid wastes at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be included. One may make 	Work site / during the construction period	√

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	<p>reference to ETWB TCW No.31/2004 for details;</p> <ul style="list-style-type: none"> the large amount of C&D waste generated is mainly due to the piling works of large diameter piles' excavation at the sea front site. If however marine sediment is found during pile excavation, the handling and disposal of such wastes will be managed in accordance with the requirements of the DASO and the current ETWB Tech. Circular no. 34/2002. 		
Waste	<p><u>Chemical Wastes</u></p> <p>If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the <i>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</i>. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. For this Project, the amount of chemical wastes produced would be small.</p>	Work site / during the construction period	√
<i>Operational Phase</i>			
Waste	<p><u>General Refuse</u></p> <p>Similar to the existing situation, the main waste type generated during the operation stage of the Project will be general refuse generated by the public and staff. These include waste paper, food wrappings and beverage containers. The disposal of future waste arisings generated at the HKCEC would follow the existing handling and disposal arrangement. Provided proper</p>	Work site / during the construction period	NA

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	arrangements are made with licensed contractors to collect the generated waste, adverse waste-related impact is not anticipated during the operation stage. It is expected that there will be a 5-7% increase ratio in the future operations.		
<i>Construction Phase</i>			
Landscape & Visual	Due consideration of appearance and view to 'hide' the construction through careful use of: (a) hoarding design; (b) temporary partition walls; (c) screen for hotels; and (d) temporary footbridge.	Entire works area and adjacent hotels	√
Landscape & Visual	Due consideration to protect existing trees.	Entire works area	√
Landscape & Visual	Due consideration of visual impact from construction activities: (a) construction workers access to reach construction areas without passing through hotels and existing HKCEC; and (b) construction light.	Entire works area	√
<i>Operational Phase</i>			
Landscape & Visual	Sensitive soft and hard landscape design for exposed rooftop garden and shady covered area underneath the Atrium Link Extension. Maximize greening opportunity via various in-situ planting and potted planting to achieve 30% of the roof area as planting area for the project.	Roof top and area underneath the Atrium Link Extension	NA
Landscape & Visual	Sensitive building architecture to visually reduce the bulkiness of the building structure, to visually break down the scale of the facades, and to create rooftops for greening opportunities.	Building of the Atrium Link Extension	NA
Landscape & Visual	Appearance and view considerations: (a) avoid industrial feel of building service elements;	Entire proposed works and adjacent hotels	NA

ANNEX H Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	(b) interior visual screens for lower levels of the hotels; (c) consider relocation of facilities of interior spaces of hotels; and (d) careful lighting design at roofs and for building façade to avoid night-time glare.		
Landscape & Visual	Transplanting of trees to adjacent locations.	Convention Avenue	NA
Landscape & Visual	Reinstatement of existing waterfront public footpaths along Convention Avenue and the existing open spaces near Fenwick Street.	Convention Avenue and Fenwick Street	NA

Remark:

- √ Compliance of Mitigation Measures
- ◇ Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Hip Hing – Ngo Kee JV
- Δ Deficiency of Mitigation Measures but rectified by Hip Hing – Ngo Kee JV
- NA Not Applicable

Annex I

24-hour TSP Monitoring Results

Figure I1 - Measured 24-hour TSP Concentration (μgm^{-3}) at AM1

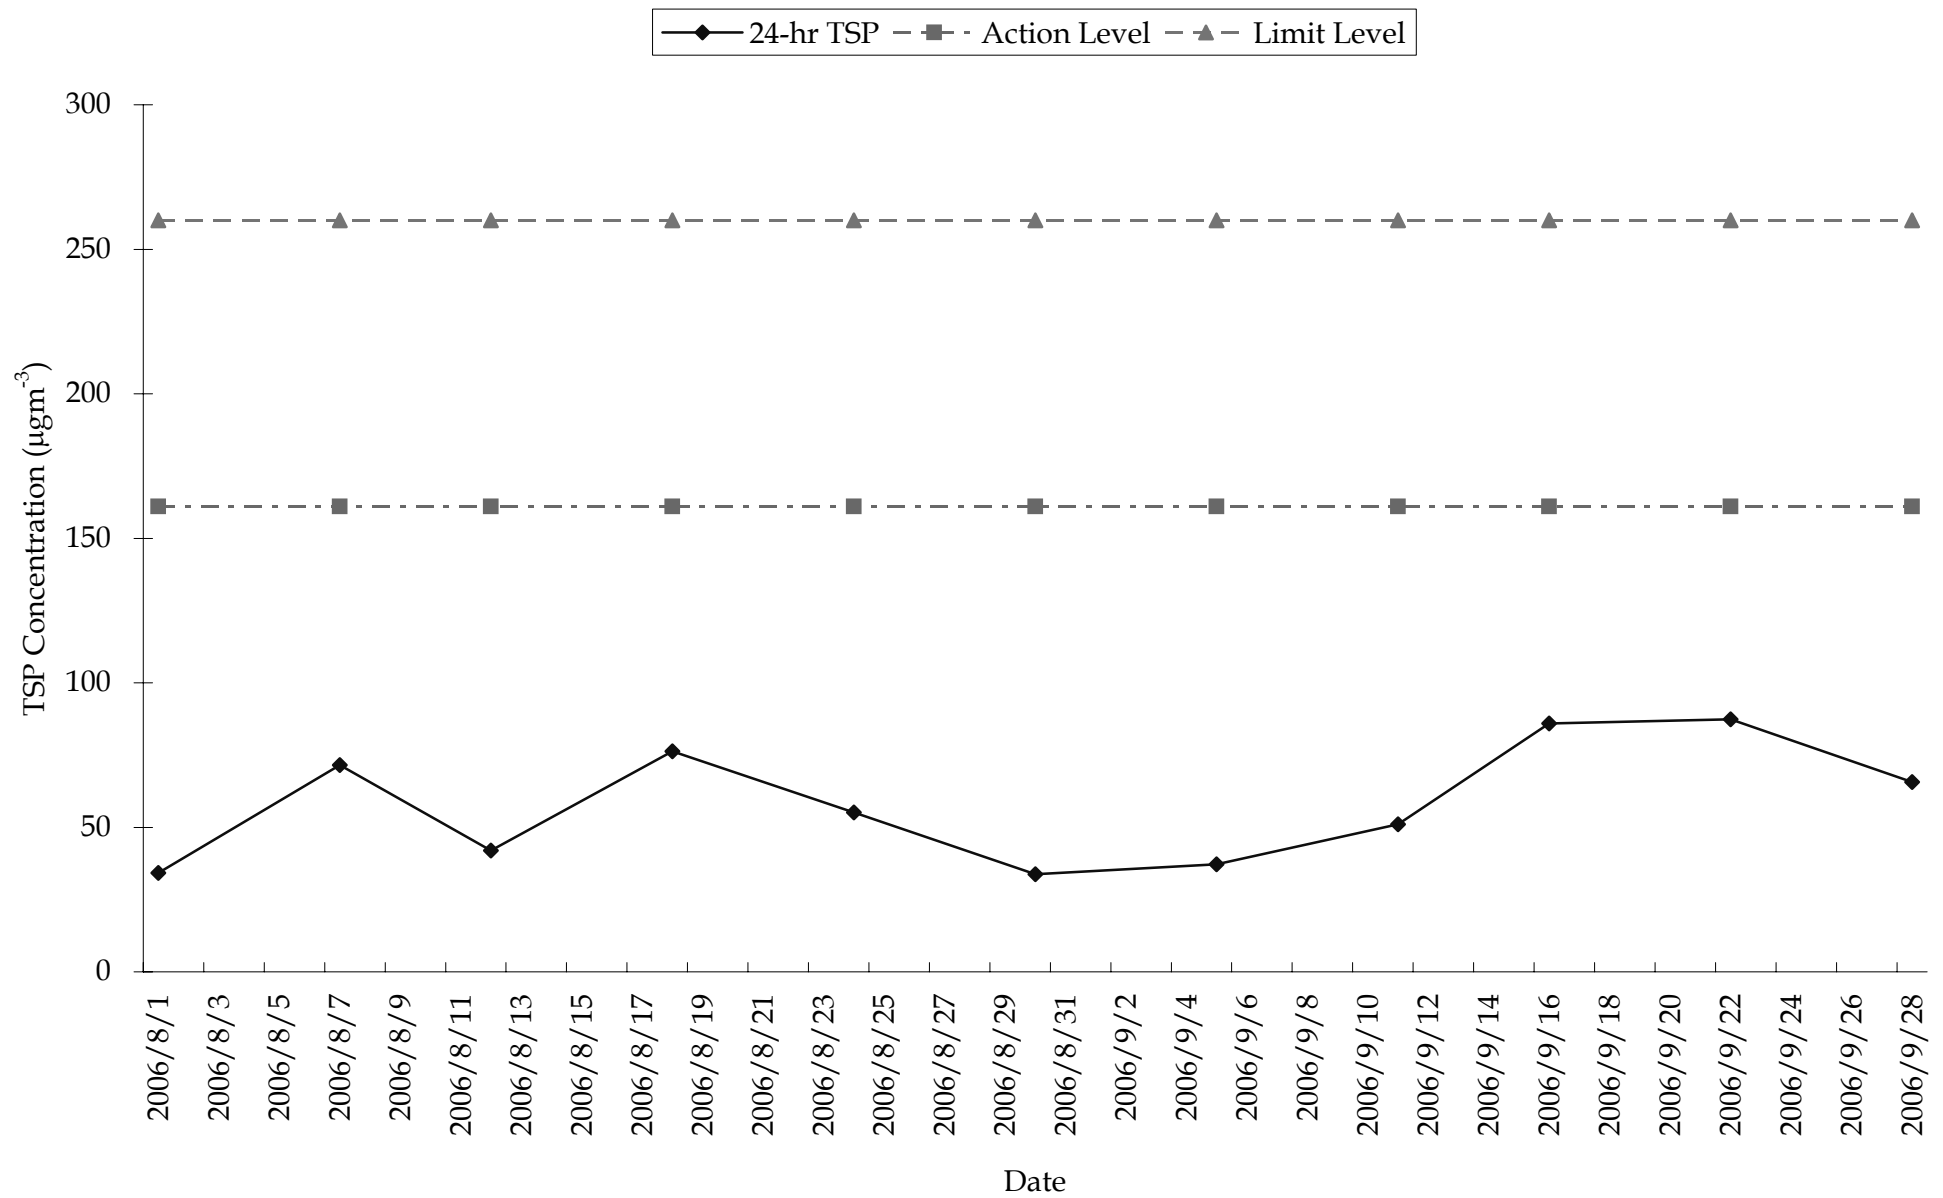


Figure I2 - Measured 24-hour TSP Concentration (μgm^{-3}) at AM2

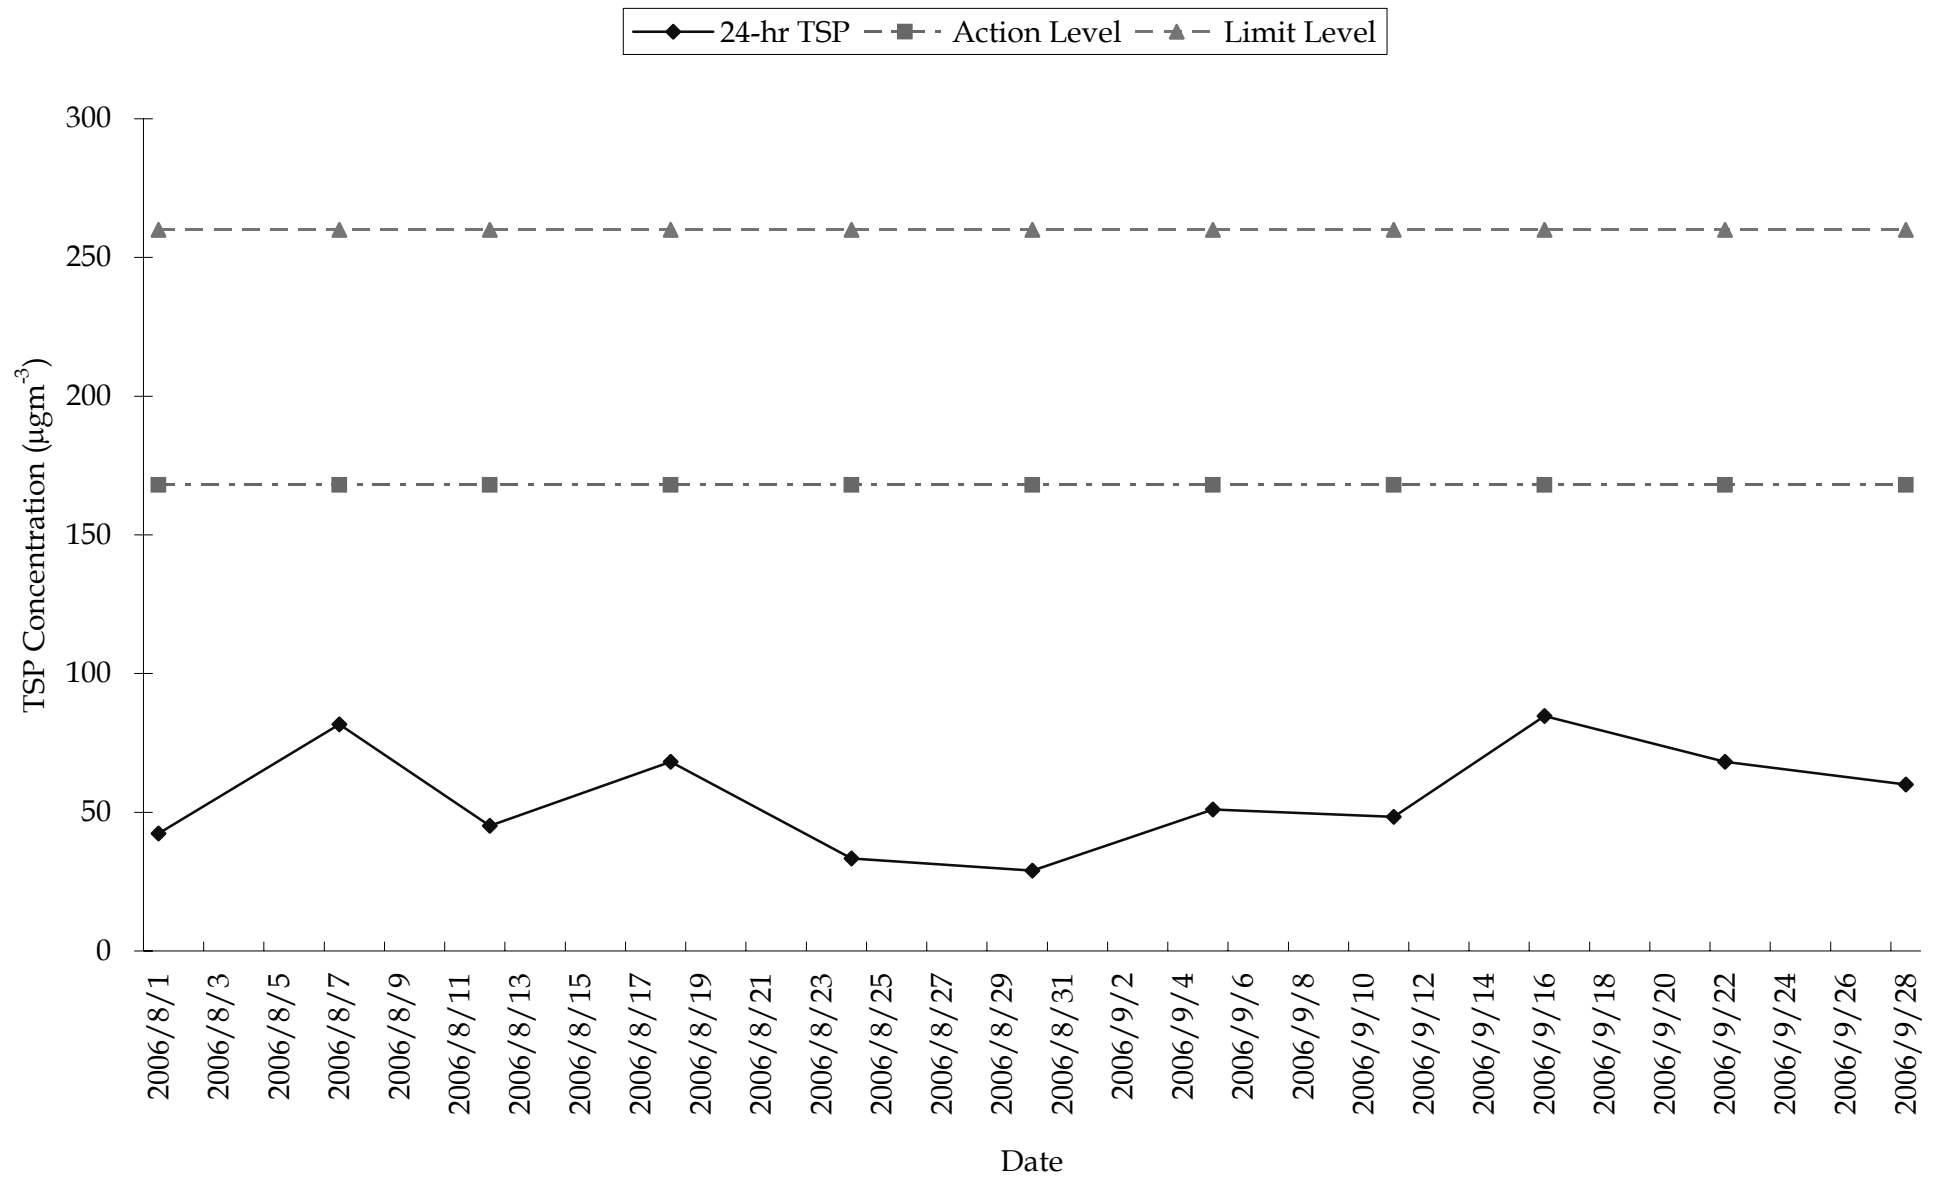


Figure I3 - Measured 1-hour TSP Concentration (μgm^{-3}) at AM1


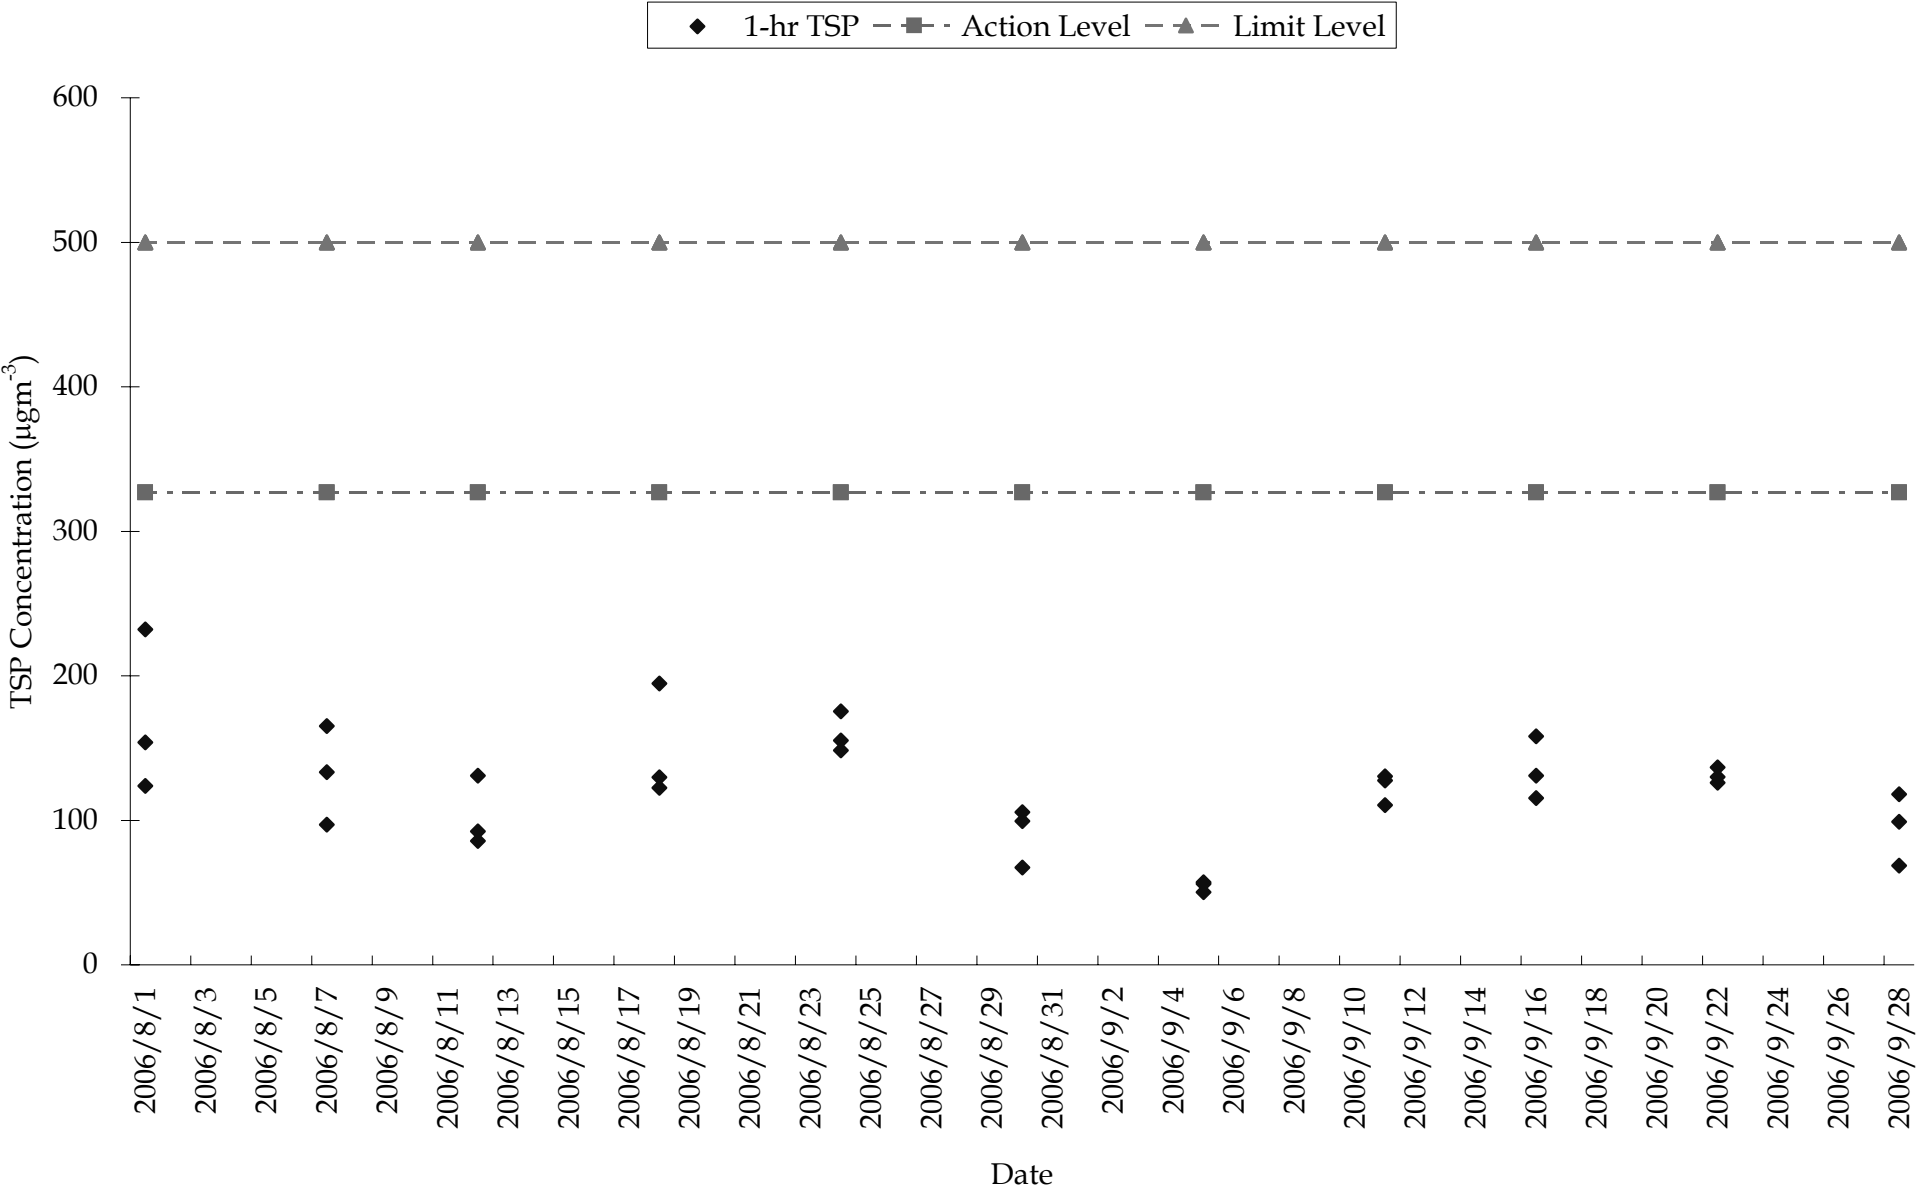


Figure I4 - Measured 1-hour TSP Concentration (μgm^{-3}) at AM2

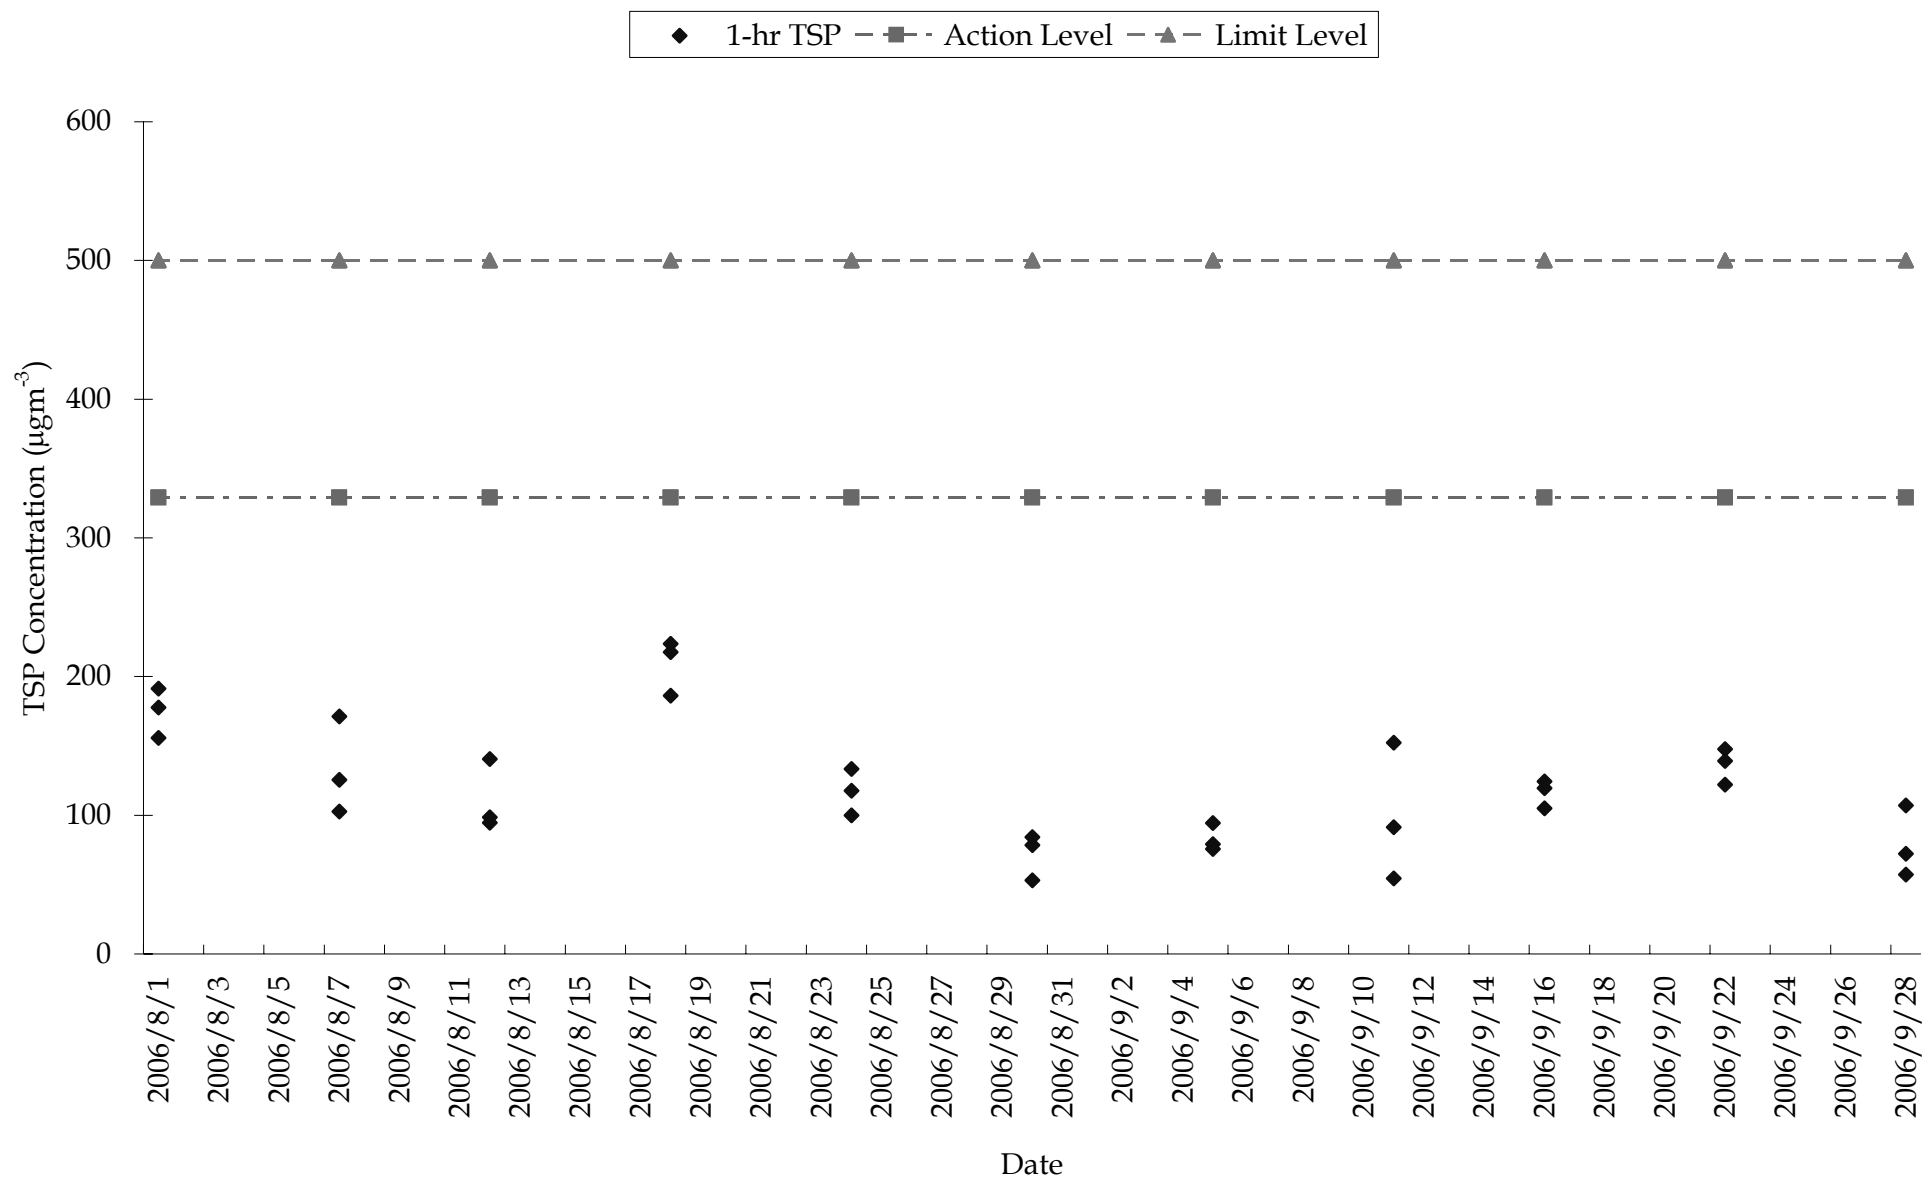

Annex I - 24-hr TSP Monitoring Results

24-hour TSP Monitoring Results at Station AM1 (Nearby The Grand Hyatt)

Date	Filter Weight (g)		Flow Rate (m ³ /min.)		Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Weather Condition	Ave. Air Temp. (°C)	Particulate weight(g)	Av. flow (m ³ /min)	Total vol. (m ³)
	Initial	Final	Initial	Final	Initial	Final							
05-Sep-06	2.8972	2.9514	1.01	1.01	10509.1	10533.1	24.0	37	Rainy	28.9	0.0542	1.01	1455.0
11-Sep-06	2.8711	2.9479	1.04	1.04	10536.1	10560.1	24.0	51	Sunny	24.4	0.0768	1.04	1502.7
16-Sep-06	2.8916	3.0209	1.04	1.04	10563.1	10587.1	24.0	86	Sunny	26.7	0.1293	1.04	1504.0
22-Sep-06	2.8941	3.0175	0.98	0.98	10590.1	10614.1	24.0	87	Sunny	26.8	0.1234	0.98	1412.6
28-Sep-06	2.8762	2.9690	0.98	0.98	10617.1	10641.1	24.0	66	Sunny	25.9	0.0928	0.98	1412.6
								Min	37				
								Max	37				
								Average	37				

24-hour TSP Monitoring Results at Station AM2 (Nearby Renaissance Harbour View Hotel)

Date	Filter Weight (g)		Flow Rate (m ³ /min.)		Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Weather Condition	Ave. Air Temp. (°C)	Particulate weight(g)	Av. flow (m ³ /min)	Total vol. (m ³)
	Initial	Final	Initial	Final	Initial	Final							
05-Sep-06	2.9081	2.9843	1.04	1.04	8935.0	8958.9	24.0	51	Rainy	28.9	0.0762	1.04	1495.1
11-Sep-06	2.8944	2.9688	1.07	1.07	8961.9	8985.9	24.0	48	Sunny	24.4	0.0744	1.07	1538.7
16-Sep-06	2.8790	3.0456	1.37	1.37	8988.9	9012.9	24.0	85	Sunny	26.7	0.1666	1.37	1967.9
22-Sep-06	2.9060	3.0349	1.31	1.31	9015.9	9039.9	24.0	68	Sunny	26.8	0.1289	1.31	1889.3
28-Sep-06	2.8751	2.9909	1.34	1.34	9042.9	9066.9	24.0	60	Sunny	25.9	0.1158	1.34	1928.2
								Min	51				
								Max	51				
								Average	51				

Annex I - 24-hr TSP Monitoring Results

24-hour TSP Monitoring Results at Station AM1 (Nearby The Grand Hyatt)

Date	Filter Weight (g)		Flow Rate (m ³ /min.)		Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Weather Condition	Ave. Air Temp. (°C)	Particulate weight(g)	Av. flow (m ³ /min)	Total vol. (m ³)
	Initial	Final	Initial	Final	Initial	Final							
05-Sep-06	2.9090	2.9119	0.98	0.98	10506.1	10507.1	1.0	50	Rainy	28.9	0.0029	0.98	57.6
05-Sep-06	2.9056	2.9091	1.04	1.04	10507.1	10508.1	1.0	56	Rainy	28.9	0.0035	1.04	62.4
05-Sep-06	2.9213	2.9250	1.08	1.08	10508.1	10509.1	1.0	57	Rainy	28.9	0.0037	1.08	64.8
11-Sep-06	2.8994	2.9063	1.04	1.04	10533.1	10534.1	1.0	111	Sunny	24.4	0.0069	1.04	62.4
11-Sep-06	2.8936	2.9011	0.98	0.98	10534.1	10535.1	1.0	128	Sunny	24.4	0.0075	0.98	58.8
11-Sep-06	2.9241	2.9320	1.01	1.01	10535.1	10536.1	1.0	130	Sunny	24.4	0.0079	1.01	60.6
16-Sep-06	2.8796	2.8895	1.04	1.04	10560.1	10561.1	1.0	158	Sunny	26.7	0.0099	1.04	62.6
16-Sep-06	2.8921	2.8991	1.01	1.01	10561.1	10562.1	1.0	115	Sunny	26.7	0.0070	1.01	60.7
16-Sep-06	2.8690	2.8772	1.04	1.04	10562.1	10563.1	1.0	131	Sunny	26.7	0.0082	1.04	62.6
22-Sep-06	2.8892	2.8971	1.04	1.04	10587.1	10588.1	1.0	126	Sunny	26.8	0.0079	1.04	62.6
22-Sep-06	2.9012	2.9095	1.01	1.01	10588.1	10589.1	1.0	137	Sunny	26.8	0.0083	1.01	60.7
22-Sep-06	2.8954	2.9033	1.01	1.01	10589.1	10590.1	1.0	130	Sunny	26.8	0.0079	1.01	60.7
28-Sep-06	2.8736	2.8810	1.04	1.04	10614.1	10615.1	1.0	118	Sunny	25.9	0.0074	1.04	62.6
28-Sep-06	2.8986	2.9029	1.04	1.04	10615.1	10616.1	1.0	69	Sunny	25.9	0.0043	1.04	62.6
28-Sep-06	2.8886	2.8948	1.04	1.04	10616.1	10617.1	1.0	99	Sunny	25.9	0.0062	1.04	62.6
								Min	50				
								Max	130				
								Average	89				

24-hour TSP Monitoring Results at Station AM2 (Nearby Renaissance Harbour View Hotel)


Date	Filter Weight (g)		Flow Rate (m ³ /min.)		Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Weather Condition	Ave. Air Temp. (°C)	Particulate weight(g)	Av. flow (m ³ /min)	Total vol. (m ³)
	Initial	Final	Initial	Final	Initial	Final							
05-Sep-06	2.9065	2.9110	0.99	0.99	8932.0	8933.0	1.0	76	Rainy	28.9	0.0045	0.99	59.4
05-Sep-06	2.9180	2.9227	0.99	0.99	8933.0	8934.0	1.0	79	Rainy	28.9	0.0047	0.99	59.4
05-Sep-06	2.8928	2.8984	0.99	0.99	8934.0	8935.0	1.0	94	Rainy	28.9	0.0056	0.99	59.4
11-Sep-06	2.8942	2.9037	1.04	1.04	8958.9	8959.9	1.0	152	Sunny	24.4	0.0095	1.04	62.4
11-Sep-06	2.9096	2.9153	1.04	1.04	8959.9	8960.9	1.0	91	Sunny	24.4	0.0057	1.04	62.4
11-Sep-06	2.8860	2.8894	1.04	1.04	8960.9	8961.9	1.0	54	Sunny	24.4	0.0034	1.04	62.4
16-Sep-06	2.8902	2.9002	1.34	1.34	8985.9	8986.9	1.0	124	Sunny	26.7	0.0100	1.34	80.3
16-Sep-06	2.9157	2.9243	1.37	1.37	8986.9	8987.9	1.0	105	Sunny	26.7	0.0086	1.37	82.0
16-Sep-06	2.9078	2.9174	1.34	1.34	8987.9	8988.9	1.0	119	Sunny	26.7	0.0096	1.34	80.3
22-Sep-06	2.8985	2.9085	1.37	1.37	9012.9	9013.9	1.0	122	Sunny	26.8	0.0100	1.37	82.0
22-Sep-06	2.8747	2.8868	1.37	1.37	9013.9	9014.9	1.0	148	Sunny	26.8	0.0121	1.37	82.0
22-Sep-06	2.8853	2.8967	1.37	1.37	9014.9	9015.9	1.0	139	Sunny	26.8	0.0114	1.37	82.0
28-Sep-06	2.8846	2.8932	1.34	1.34	9039.9	9040.9	1.0	107	Sunny	25.9	0.0086	1.34	80.3
28-Sep-06	2.8805	2.8851	1.34	1.34	9040.9	9041.9	1.0	57	Sunny	25.9	0.0046	1.34	80.3
28-Sep-06	2.8634	2.8692	1.34	1.34	9041.9	9042.9	1.0	72	Sunny	25.9	0.0058	1.34	80.3
								Min	54				
								Max	152				
								Average	91				

Annex I - Meteorological Data Extracted from King's Park Stations of the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C)	Average Wind Speed (km/h)	Average Relative Humidity (%)	Total Rainfall (mm)	Wind Direction
05-Sep-06	Rainy	28.9	6.0	79.5	3.2	W
11-Sep-06	Sunny	24.4	12.0	75.5	0	NE
16-Sep-06	Sunny	26.7	8.0	76.0	0	NE
22-Sep-06	Sunny	26.8	10.0	72.5	0	E
28-Sep-06	Sunny	25.9	12.0	71.0	0	E

Annex J

Laboratory Report of Water Quality Sampling

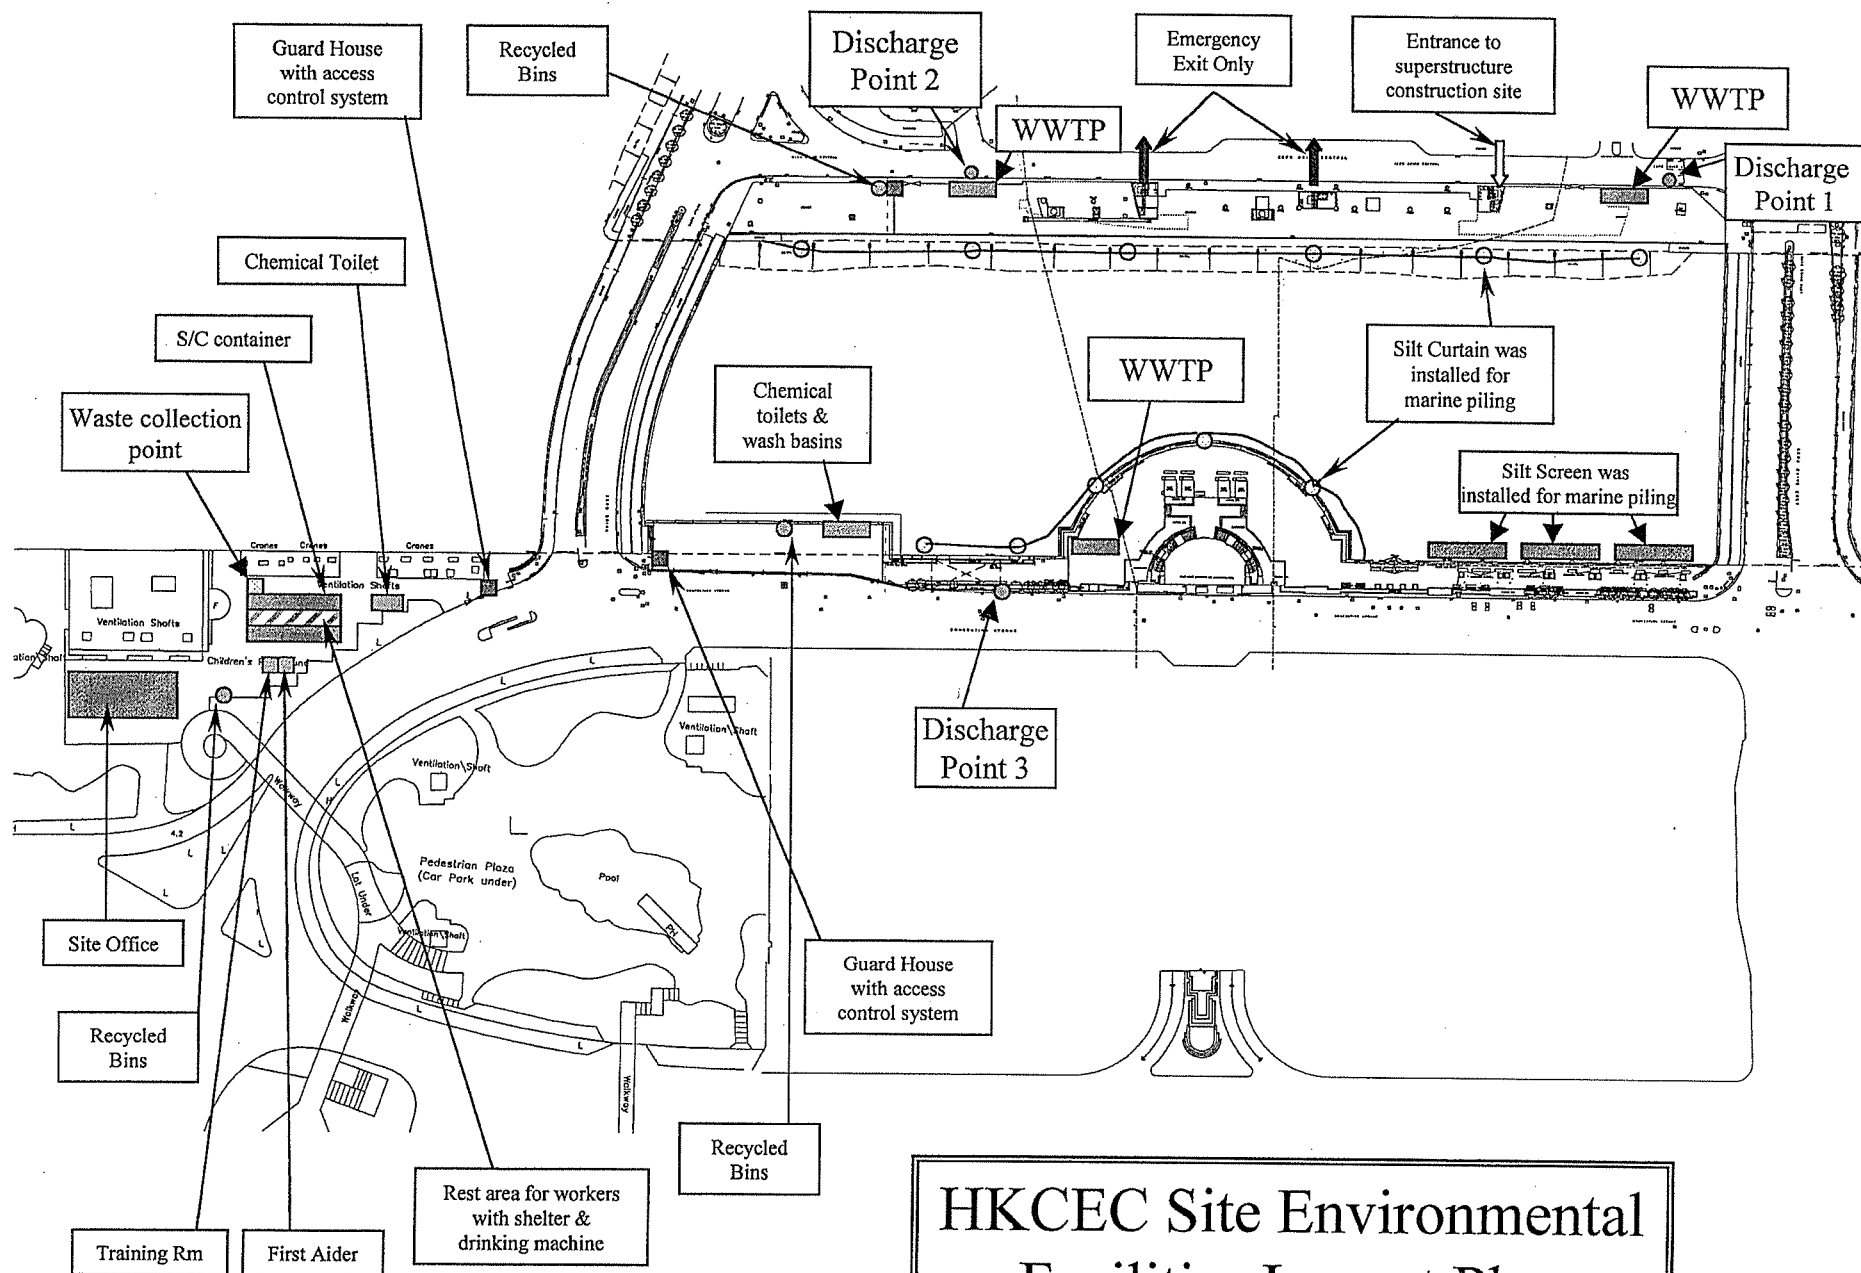

HKCEC Site Environmental Facilities Layout Plan

(1-Aug-06)



ENVIRO LABS LIMITED

環境化驗有限公司

TEST REPORT

JOB NO. : A-61003A-1
 DATE OF ISSUE : 29 September 2006
 PAGE : 1 of 1

1. Customer

Hip Hing - Ngo Kee Joint Venture
 29/F, New World Tower, 16-18 Queen's Road Central, Hong Kong
 Attn.: Mr. Ken Leung

2. Sample Identification

Sample Description : 1 batch of water sample said to be wastewater was received in cool condition
 Quantity of Sample : 1 x 1L in plastic bottle (for TSS) and 1 x 250mL in plastic bottle (for COD)
 Sampling : Conducted by the staff of the Enviro Labs Ltd.
 Sampling Point : Outlet of Wastewater Treatment Facility
 (HKCEC Expansion Project, H200605)
 Preservation : Stored under refrigerated condition, COD: conc. H₂SO₄ was added to pH < 2
 Sampling Date : 7 September 2006
 Received Date & Time : 7 September 2006 18:00

3. Test Method

Parameter	Reference Method	Testing Period
(i) pH	APHA ¹ 20e 4500 H*B	7 Sep 2006 (On-site)
(ii) Total Suspended Solids (TSS) Dried at 103-105°C	APHA ¹ 17e 2540 D	7 - 12 Sep 2006
(iii) Chemical Oxygen Demand (COD)	APHA ¹ 20e 5220 C	7 - 14 Sep 2006

1. APHA Standard Methods for the Examination of Water and Wastewater

4. Test Result (1)*

Label marked by client	Test Parameter	Sample No.	Test Result	Discharge Limit **	Unit
HKCEC Expansion Project H200605 Sample (1)	pH at 25 °C	61003-1	7.0	6 - 9	—
	TSS	61003-1	17	≤30	mg/L
	COD	61003-2	< 50	≤80	mgO ₂ /L


* Test results relate only to the items received.

** Information provided by the customer. (It is not a test result, information for reference only).

— END of REPORT —



APPROVED SIGNATORY:


 Kenneth Kar Kin LAM
 (Laboratory Manager)



ENVIRO LABS LIMITED

環境化驗有限公司

TEST REPORT

JOB NO. : A-61003A-2
 DATE OF ISSUE : 29 September 2006
 PAGE : 1 of 1

1. Customer

Hip Hing - Ngo Kee Joint Venture
 29/F, New World Tower, 16-18 Queen's Road Central, Hong Kong
 Attn.: Mr. Ken Leung

2. Sample Identification

Sample Description : 1 batch of water sample said to be wastewater was received in cool condition
 Quantity of Sample : 1 x 1L in plastic bottle (for TSS) and 1 x 250mL in plastic bottle (for COD)
 Sampling : Conducted by the staff of the Enviro Labs Ltd.
 Sampling Point : Outlet of Wastewater Treatment Facility
 (HKCEC Expansion Project, H200605)
 Preservation : Stored under refrigerated condition, COD: conc. H₂SO₄ was added to pH < 2
 Sampling Date : 7 September 2006
 Received Date & Time : 7 September 2006 18:00

3. Test Method

Parameter	Reference Method	Testing Period
(i) pH	APHA ¹ 20e 4500 H ⁺ B	7 Sep 2006 (On-site)
(ii) Total Suspended Solids (TSS) Dried at 103-105°C	APHA ¹ 17e 2540 D	7 - 12 Sep 2006
(iii) Chemical Oxygen Demand (COD)	APHA ¹ 20e 5220 C	7 - 14 Sep 2006

1. APHA Standard Methods for the Examination of Water and Wastewater

4. Test Result (1)*

Label marked by client	Test Parameter	Sample No.	Test Result	Discharge Limit **	Unit
HKCEC Expansion Project H200605 Sample (2)	pH at 25 °C	61003-3	7.4	6 - 9	--
	TSS	61003-3	8.8	≤30	mg/L
	COD	61003-4	< 50	≤80	mgO ₂ /L

* Test results relate only to the items received.

** Information provided by the customer. (It is not a test result, information for reference only).

— END OF REPORT —



APPROVED SIGNATORY :

Kenneth Kar Kin LAM
 (Laboratory Manager)

Annex K

Waste Flow Table

HKCEC – Atrium Link Extension Project

Name of Project Proponent: HKTDC

Project Commencement Date: 1 Aug 2006

Construction Completion Date: March 2009

Monthly Summary Waste Flow Table for Year 2006

Year	Actual Quantities of inert C&D Materials (in 10 ³ Kg) ⁽¹⁾					Actual Quantities of C&D Wastes (in 10 ³ Kg) ⁽⁴⁾									
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Steel Materials (Demolition of footbridge)	Paper/cardboard packaging		Steel Materials (Demolition of existing Atrium Link)		Chemical Waste		Steel Materials (Demolition of Working Platform)	General refuse	Other waste
	(a)	(b)	(c)	(d)	(a)-(b)-(c)-(d)	Disposal	Recycle	Disposal	Recycle	Disposal	Recycle	Disposal	Disposal	Disposal	Disposal
January	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
February	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
March	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
April	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
May	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
June	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
July	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
August	264	0	1	0	263	0	0	1	N/A	N/A	N/A	0	N/A	50	81
September	1509 ⁽²⁾	0	2 ⁽³⁾	0	1507	0	0	1	N/A	N/A ⁽⁵⁾	N/A ⁽⁵⁾	0	N/A	60	215 ⁽⁶⁾
October	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
November	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
December	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Total	1773	0	3	0	1770	0	0	2	N/A	N/A	N/A	0	N/A	110	296

Note: ⁽¹⁾ Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil

⁽²⁾ Inert C&D material mainly generated from construction of foundation.

⁽³⁾ Reused for building bunds and making sand bags.

⁽⁴⁾ Non-inert C&D material include steel materials generated from demolition, paper / cardboard packaging waste, chemical waste and other wastes such as general refuse.

⁽⁵⁾ As only Foundation work is being carried out, no steel materials were generated.

⁽⁶⁾ Wastes including 60 tonnes of general refuse, and 215 tonnes of waste due to A&A works of HKCEC including demolition of equipment (E&M services) and finishing material.

Annex L

Construction Programme for Next Three Months

Hong Kong Convention and Exhibition Centre Expansion Project 3 Months Rolling Programme (2006-08-11 to 2006-11-10)					Gantt Chart																											
ID	Task Name	Duration	Start	Finish	June				July				August				September				October				N							
					21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5			
1	PROJECT WIDE	827 days	26/5/2006	11/3/2009																												
2	Critical Dates	827 days	26/5/2006	11/3/2009																												
3	Project Milestones	827 days	26/5/2006	11/3/2009																												
9	Commencement of Bored Pile Works	0 days	13/10/2006	13/10/2006																												
10	RIP for GBP With Fire Engineering Approval	0 days	16/9/2006	16/9/2006																												
36	Durations	827 days	26/5/2006	11/3/2009																												
37	Contract Duration to Meet KD 1	919 edays	26/5/2006	30/11/2008																												
38	Contract Duration to Meet KD 2	1020 edays	26/5/2006	11/3/2009																												
39	Contract Duration to Meet KD 3	1020 edays	26/5/2006	11/3/2009																												
40	DETAIL DESIGN	243 days	25/5/2006	16/3/2007																												
41	Design Submission & Approval (Temporary Works)	215 days	26/5/2006	13/2/2007																												
42	Temporary Hoarding (Internal Area)	146 days	26/5/2006	17/11/2006																												
47	For Pedestrian Access Beside Existing Main Truss	51 days	23/6/2006	22/8/2006																												
48	WP Hoarding Design Preparation & Submission	17 days	23/6/2006	13/7/2006																												
49	Design Check by Independent Checking Engineer	26 days	14/7/2006	12/8/2006																												
50	DDR for Hoarding Plan for PM	8 days	14/8/2006	22/8/2006																												
51	For GL 17/A&B Columns Construction	44 days	1/9/2006	24/10/2006																												
52	WP Hoarding Design Preparation & Submission	20 days	1/9/2006	23/9/2006																												
53	Design Check by Independent Checking Engineer	12 days	25/9/2006	10/10/2006																												
54	DDR for Hoarding Plan for PM	12 days	11/10/2006	24/10/2006																												
55	For New Pedestrian Diversion Access (Beside A1 Truss)	44 days	25/9/2006	17/11/2006																												
56	WP Hoarding Design Preparation & Submission	20 days	25/9/2006	19/10/2006																												
57	Design Check by Independent Checking Engineer	12 days	20/10/2006	3/11/2006																												
58	DDR for Hoarding Plan for PM	12 days	4/11/2006	17/11/2006																												
59	Temporary Hoarding (Ground Floor)	154 days	26/5/2006	27/11/2006																												
65	For Others Area	59 days	16/9/2006	27/11/2006																												
66	Hoarding Design Preparation & Submission	35 days	16/9/2006	28/10/2006																												
67	Design Check by Independent Checking Engineer	12 days	31/10/2006	13/11/2006																												
68	DDR for Hoarding Design by PM	12 days	14/11/2006	27/11/2006																												
70	Temporary Working Platform (for Roof Truss Assemble)	39 days	15/8/2006	28/9/2006																												
71	Temporary Working Platform Design (including Marine Pile Design) Preparation & Submission	15 days	15/8/2006	31/8/2006																												
72	Design Check by Design Checker	12 days	1/9/2006	14/9/2006																												
73	DDR for Temporary Platform & Foundation Plan Design by PM	12 days	15/9/2006	28/9/2006																												
74	DDR for Temporary Platform & Foundation Plan Design	0 days	28/9/2006	28/9/2006																												
75	Temporary Working Platform (for A1 Panel Truss Assemble)	39 days	28/9/2006	15/11/2006																												
76	Temporary Working Platform Design (including Marine Pile Design) Preparation & Submission	15 days	28/9/2006	17/10/2006																												
77	Design Check by Design Checker	12 days	18/10/2006	1/11/2006																												
78	DDR for Temporary Platform & Foundation Plan Design by PM	12 days	2/11/2006	15/11/2006																												
79	DDR for Temporary Platform & Foundation Plan Design	0 days	15/11/2006	15/11/2006																												
80	Temporary Pedestrian Access Platform in Phase 2	55 days	25/10/2006	30/12/2006																												
81	Access Platform Preparation & Submission																															

Hong Kong Convention and Exhibition Centre Expansion Project 3 Months Rolling Programme (2006-08-11 to 2006-11-10)																												
ID	Task Name	Duration	Start	Finish	June					July					August					September				October				N
					21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	
86	Submission of FER to Design Checker	12 days	18/8/2006	31/8/2006																								
87	Submission to PM	3 days	1/9/2006	4/9/2006																								
88	Approval from PM	0 days	4/9/2006	4/9/2006																								
89	Fire Engineering Report C (Tunnel)	58 days	18/8/2006	26/10/2006																								
90	Preparation of Fire Engineering Report C	40 days	18/8/2006	4/10/2006																								
91	Submission of FER to Design Checker	12 days	5/10/2006	19/10/2006																								
92	Submission to PM	6 days	20/10/2006	26/10/2006																								
93	Approval from PM	0 days	26/10/2006	26/10/2006																								
94	Demolition Plan	208 days	26/5/2006	1/2/2007																								
95	Demolition of Existing Phase II Projection (GL16)	67 days	26/5/2006	14/8/2006																								
96	BS Diversion Plan	39 days	26/5/2006	12/7/2006																								
97	Design BS Diversion Preparation & Submission	27 days	26/5/2006	27/6/2006																								
98	Design Check by Design Checker	7 days	26/6/2006	4/7/2006																								
99	RIP / DDR by PM and HKCEC	7 days	5/7/2006	12/7/2006																								
100	RIP / DDR for Diversion Plan	0 days	12/7/2006	12/7/2006																								
101	Demolition Plan	67 days	26/5/2006	14/8/2006																								
102	Detailed Design Preparation	15 days	26/5/2006	13/6/2006																								
103	Design Check by Design Checker	27 days	5/6/2006	6/7/2006																								
104	RIP/ DDR for Submission by PM	33 days	7/7/2006	14/8/2006																								
105	RIP / DDR for Demolition Plan	0 days	14/8/2006	14/8/2006																								
106	Demolition of Existing West Glass Wall at Atrium Link	49 days	17/7/2006	11/9/2006																								
107	BS Diversion Plan	36 days	1/8/2006	11/9/2006																								
108	Design BS Diversion Preparation & Submission	12 days	1/8/2006	14/8/2006																								
109	Design Check by Design Checker	12 days	15/8/2006	28/8/20																								

Hong Kong Convention and Exhibition Centre Expansion Project 3 Months Rolling Programme (2006-08-11 to 2006-11-10)					Gantt Chart																											
ID	Task Name	Duration	Start	Finish	June					July					August					September					October					N		
					21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5			
139	Submission to BD	28 days	23/9/2006	27/10/2006																												
140	Structural Detailed Design Preparation	18 days	9/9/2006	29/9/2006																												
141	Design Check by Design Checker	12 days	30/9/2006	16/10/2006																												
142	Submission to BD	22 days	17/10/2006	11/11/2006																												
144	DDR for Submission by PM	24 days	17/10/2006	14/11/2006																												
146	A&A Works for HKCEC Phase 2	86 days	25/9/2006	9/1/2007																												
147	A&A Works Design Preparation & Submission	31 days	25/9/2006	2/11/2006																												
148	Design Check by Design Checker	9 days	3/11/2006	13/11/2006																												
149	RIP for PM	13 days	14/11/2006	28/11/2006																												
150	RIP by A&A Plan	0 days	28/11/2006	28/11/2006																												
151	Detailed Design Preparation	30 days	31/10/2006	4/12/2006																												
152	Design Check by Design Checker	7 days	5/12/2006	12/12/2006																												
155	Heavy Lifting & Sliding System for Steel Roof Trusses	84 days	1/11/2006	13/2/2007																												
156	Heavy Lifting Design & Sliding System Design Preparation & Submission	24 days	1/11/2006	28/11/2006																												
157	Design Check by Independent Checking Engineer	6 days	29/11/2006	5/12/2006																												
158	RIP by PM	12 days	6/12/2006	19/12/2006																												
159	RIP for Heavy Lifting Method and Sliding System	0 days	19/12/2006	19/12/2006																												
160	Detailed Design Preparation	24 days	20/12/2006	19/1/2007																												
165	Pontoons for Construction Works	34 days	7/8/2006	14/9/2006																												
166	Pontoons Design Preparation & Submission	7 days	7/8/2006	31/8/2006																												
167	Design Check by Independent Checking Engineer	6 days	1/9/2006	7/9/2006																												
168	DDR for Pontoons by PM	6 days	8/9/2006	14/9/2006																												
172	Design Submission & Approval (Permanent Works)	243 days	25/5/2006	16/3/2007																												

Hong Kong Convention and Exhibition Centre
Expansion Project
3 Months Rolling Programme
(2006-08-11 to 2006-11-10)

ID	Task Name	Duration	Start	Finish	21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5	N
199	Foundation / ELS Design Preparation & Submission	14 days	26/5/2006	12/6/2006																										
200	Design Check by Design Checker	20 days	13/6/2006	6/7/2006																										
201	RIP & DDR for Foundation / ELS Design by PM	11 days	7/7/2006	19/7/2006																										
202	RIP & DDR for Foundation / ELS Plan	0 days	19/7/2006	19/7/2006																										
208	Foundation / ELS Design (BP4 and BP5)	92 days	26/5/2006	12/9/2006																										
209	Foundation / ELS Design Preparation & Submission	14 days	26/5/2006	12/6/2006																										
210	Submit to MTRC for Endorsement/Comments	21 days	26/5/2006	20/6/2006																										
211	Design Check by Design Checker	11 days	13/6/2006	24/6/2006																										
212	Submission to MTRC for Endorsement/Comments	10 days	29/6/2006	11/7/2006																										
213	Further Design Check by Design Checker	40 days	5/7/2006	19/8/2006																										
214	RIP & DDR for Foundation / ELS Design by PM	12 days	16/8/2006	29/8/2006																										
215	RIP & DDR for Foundation / ELS Plan	0 days	29/8/2006	29/8/2006																										
216	2 nd Submission to MTRC for Endorsement/Comments	12 days	30/8/2006	12/9/2006																										
218	Architectural Design	152 days	11/9/2006	16/3/2007																										
219	Arch - External façade and Gondola Design	89 days	15/9/2006	3/1/2007																										
220	Design Preparation & Submission	20 days	15/9/2006	10/10/2006																										
221	Design Check by Design Checker	12 days	11/10/2006	24/10/2006																										
222	RIP by PM	12 days	25/10/2006	8/11/2006																										
223	RIP for External façade and Gondola Design	0 days	8/11/2006	8/11/2006																										
224	Detailed Design Preparation	21 days	9/11/2006	2/12/2006																										
225	Design Check by Design Checker	12 days	4/12/2006	16/12/2006																										
226	DDR for DD Submission by PM	12 days	18/12/2006	3/1/2007																										
228	Arch - Landscaping	111 days	12/9/2006	25/1/2007																										
229	Schematic Design Preparation & Submission	16 days	12/9/2006	29/9/2006																										
230	Design Check by Design Checker	16 days	30/9/2006	20/10/2006																										
231	RIP by PM	12 days	21/10/2006	4/11/2006																										
232	RIP for Schemetic Design	0 days	4/11/2006	4/11/2006																										
237	Arch - Finishes (Internal & External)	146 days	18/9/2006	16/3/2007																										
238	Schematic Design Preparation & Submission	35 days	18/9/2006	31/10/2006																										
239	Design Check by Design Checker	18 days	1/11/2006	21/11/2006																										
246	Arch - Architectural Design (General Items)	131 days	11/9/2006	20/2/2007																										
247	Schematic Design Preparation & Submission	17 days	11/9/2006	29/9/2006																										
248	Design Check by Design Checker	5 days	30/9/2006	6/10/2006																										
249	RIP by PM	6 days	9/10/2006	14/10/2006																										
250	RIP for Schemetic Design	0 days	14/10/2006	14/10/2006																										
255	Arch - Fire Curtain & Smoke Curtain Schedule	115 days	11/9/2006	29/1/2007																										
256	Schematic Design Preparation & Submission	17 days	11/9/2006	29/9/2006																										
257	Design Check by Design Checker	11 days	30/9/2006	14/10/2006																										
258	RIP by PM	13 days	16/10/2006	31/10/2006																										
259	RIP for Schemetic Design	0 days	31/10/2006	31/10/2006																										
264	Arch - Door Schedule (including sliding and acoustic doors)	115 days	11/9/2006	29/1/2007																										
265	Schematic Design Preparation & Submission	17 days	11/9/2006	29/9/2006																										
266	Design Check by Design Checker	11 days	30/9/2006	14/10/2006																										
267	RIP by PM	13 days	16/10/2006	31/10/2006																										
268	RIP for Schemetic Design	0 days	31/10/2006	31/10/2006																										

Project: 3 Months Rolling Programme
Date: 25/8/2006

Task

Progress

Milestone



Summary

Rolled Up Task

Rolled Up Milestone



Rolled Up Progress

Split

External Tasks



Project Summary













Group By Summary

Deadline




Hong Kong Convention and Exhibition Centre
Expansion Project
3 Months Rolling Programme
(2006-08-11 to 2006-11-10)

ID	Task Name	Duration	Start	Finish	June							July							August							September							October							N
273	Arch - Ironmongery Schedule	100 days	11/10/2006	12/2/2007	21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5											
274	Schematic Design Preparation & Submission	16 days	11/10/2006	28/10/2006																																				
275	Design Check by Design Checker	13 days	31/10/2006	14/11/2006																																				
282	Arch - Signage and Electronic Sign	138 days	12/9/2006	1/3/2007																																				
283	Schematic Design Preparation & Submission	16 days	12/9/2006	29/9/2006																																				
284	Design Check by Design Checker	11 days	30/9/2006	14/10/2006																																				
285	RIP by PM	13 days	16/10/2006	31/10/2006																																				
286	RIP for Schemetic Design	0 days	31/10/2006	31/10/2006																																				
291	Arch - Maintenance Access System / Catwalks	91 days	11/10/2006	29/1/2007																																				
292	Schematic Design Preparation & Submission	16 days	11/10/2006	28/10/2006																																				
293	Design Check by Design Checker	13 days	31/10/2006	14/11/2006																																				
300	Structural Design	197 days	26/5/2006	19/1/2007																																				
301	Review in Principle	96 days	26/5/2006	16/9/2006																																				
302	Superstrucutre	96 days	26/5/2006	16/9/2006																																				
303	Structural Design Preparation & Submission	29 days	26/5/2006	29/6/2006																																				
304	Design Check by Design Checker	39 days	30/6/2006	15/8/2006																																				
305	RIP by PM	28 days	16/8/2006	16/9/2006																																				
306	RIP for Structural Plan	0 days	16/9/2006	16/9/2006																																				
307	Details Design Review	188 days	7/6/2006	19/1/2007																																				
308	Roof Trusses (Including Bearing Design)	87 days	7/6/2006	16/9/2006																																				
309	Detailed Design Preparation	63 days	7/6/2006	19/8/2006																																				
310	Design Check by Design Checker	10 days	21/8/2006	31/8/2006																																				
311	DDR for DD Submission by PM	14 days	1/9/2006	16/9/2006																																				
312	DDR for Structural Plan	0 days	16/9/2006	16/9/2006																																				
313	R. C. Mega Columns	59 days	7/8/2006	16/10/2006																																				
314	Detailed Design Preparation	35 days	7/8/2006	15/9/2006																																				
315	Design Check by Design Checker	12 days	16/9/2006	29/9/2006																																				
316	DDR Submission by PM	12 days	30/9/2006	16/10/2006																																				
317	DDR for Structural Plan	0 days	16/10/2006	16/10/2006																																				
318	Floor Structure (Grid A1-A/16-25)	44 days	11/9/2006	3/11/2006																																				
319	Detailed Design Preparation	20 days	11/9/2006	4/10/2006																																				
320	Design Check by Design Checker	12 days	5/10/2006	19/10/2006																																				
321	DDR Submission by PM	12 days	20/10/2006	3/11/2006																																				
322	DDR for Structural Plan	0 days	3/11/2006	3/11/2006																																				
323	Floor Structure (Remaining Area)	59 days	3/10/2006	12/12/2006																																				
324	Detailed Design Preparation	35 days	3/10/2006	14/11/2006																																				
325	Design Check by Design Checker	12 days	15/11/2006	28/11/2006																																				
328	Other R.C. Structure & Slab	59 days	9/11/2006	19/1/2007																																				
329	Detailed Design Preparation	35 days	9/11/2006	19/12/2006																																				
333	BS Design	144 days	29/6/2006	18/12/2006																																				
334	BS - HVAC	125 days	13/7/2006	8/12/2006																																				
335	Review In Principle	93 days	13/7/2006	1/11/2006																																				
336	Stage 1	70 days	13/7/2006	3/10/2006																																				
337	Schematic Design of All HVAC Installation Preparation & Submission	29 days	13/7/2006	15/8/2006																																				
338	Design Check by Design Checker	27 days	16/8/2006	15/9/2006																																				

Project: 3 Months Rolling Programme Date: 25/8/2006	Task		Summary		Rolled Up Progress		Project Summary	
	Progress		Rolled Up Task		Split		Group By Summary	
	Milestone		Rolled Up Milestone		External Tasks		Deadline	


Hong Kong Convention and Exhibition Centre Expansion Project 3 Months Rolling Programme (2006-08-11 to 2006-11-10)					Gantt Chart																											
ID	Task Name	Duration	Start	Finish	June				July				August				September				October				N							
					21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5			
339	RIP by PM	14 days	16/9/2006	3/10/2006																												
340	RIP for Schematic Design	0 days	3/10/2006	3/10/2006																												
341	Stage 2	65 days	15/8/2006	1/11/2006																												
342	Preliminary HVAC Installation Preparation & Submission	29 days	15/8/2006	16/9/2006																												
343	Design Check by Design Checker	23 days	18/9/2006	16/10/2006																												
344	RIP by PM	13 days	17/10/2006	1/11/2006																												
345	RIP for Schematic Design	0 days	1/11/2006	1/11/2006																												
346	Details Design Review	92 days	21/8/2006	8/12/2006																												
347	Detailed Design Preparation	57 days	21/8/2006	27/10/2006																												
348	Design Check by Design Checker	24 days	28/10/2006	25/11/2006																												
349	DDR for HVAC Submission by PM	11 days	27/11/2006	8/12/2006																												
350	DDR for HVAC	0 days	8/12/2006	8/12/2006																												
351	BS - Electrical	121 days	27/7/2006	18/12/2006																												
352	Review In Principle	72 days	27/7/2006	20/10/2006																												
353	Stage 1	58 days	27/7/2006	3/10/2006																												
354	Electrical System Design Preparation & Submission	19 days	27/7/2006	17/8/2006																												
355	Design Check by Design Checker	26 days	18/8/2006	16/9/2006																												
356	RIP by PM	13 days	18/9/2006	3/10/2006																												
357	RIP for Electrical System Design	0 days	3/10/2006	3/10/2006																												
358	Stage 2	56 days	15/8/2006	20/10/2006																												
359	Electrical Layouts Preparation & Submission	19 days	15/8/2006	5/9/2006																												
360	Design Check by Design Checker	25 days	6/9/2006	5/10/2006																												
361	RIP by PM	12 days	6/10/2006																													

Hong Kong Convention and Exhibition Centre
Expansion Project
3 Months Rolling Programme
(2006-08-11 to 2006-11-10)

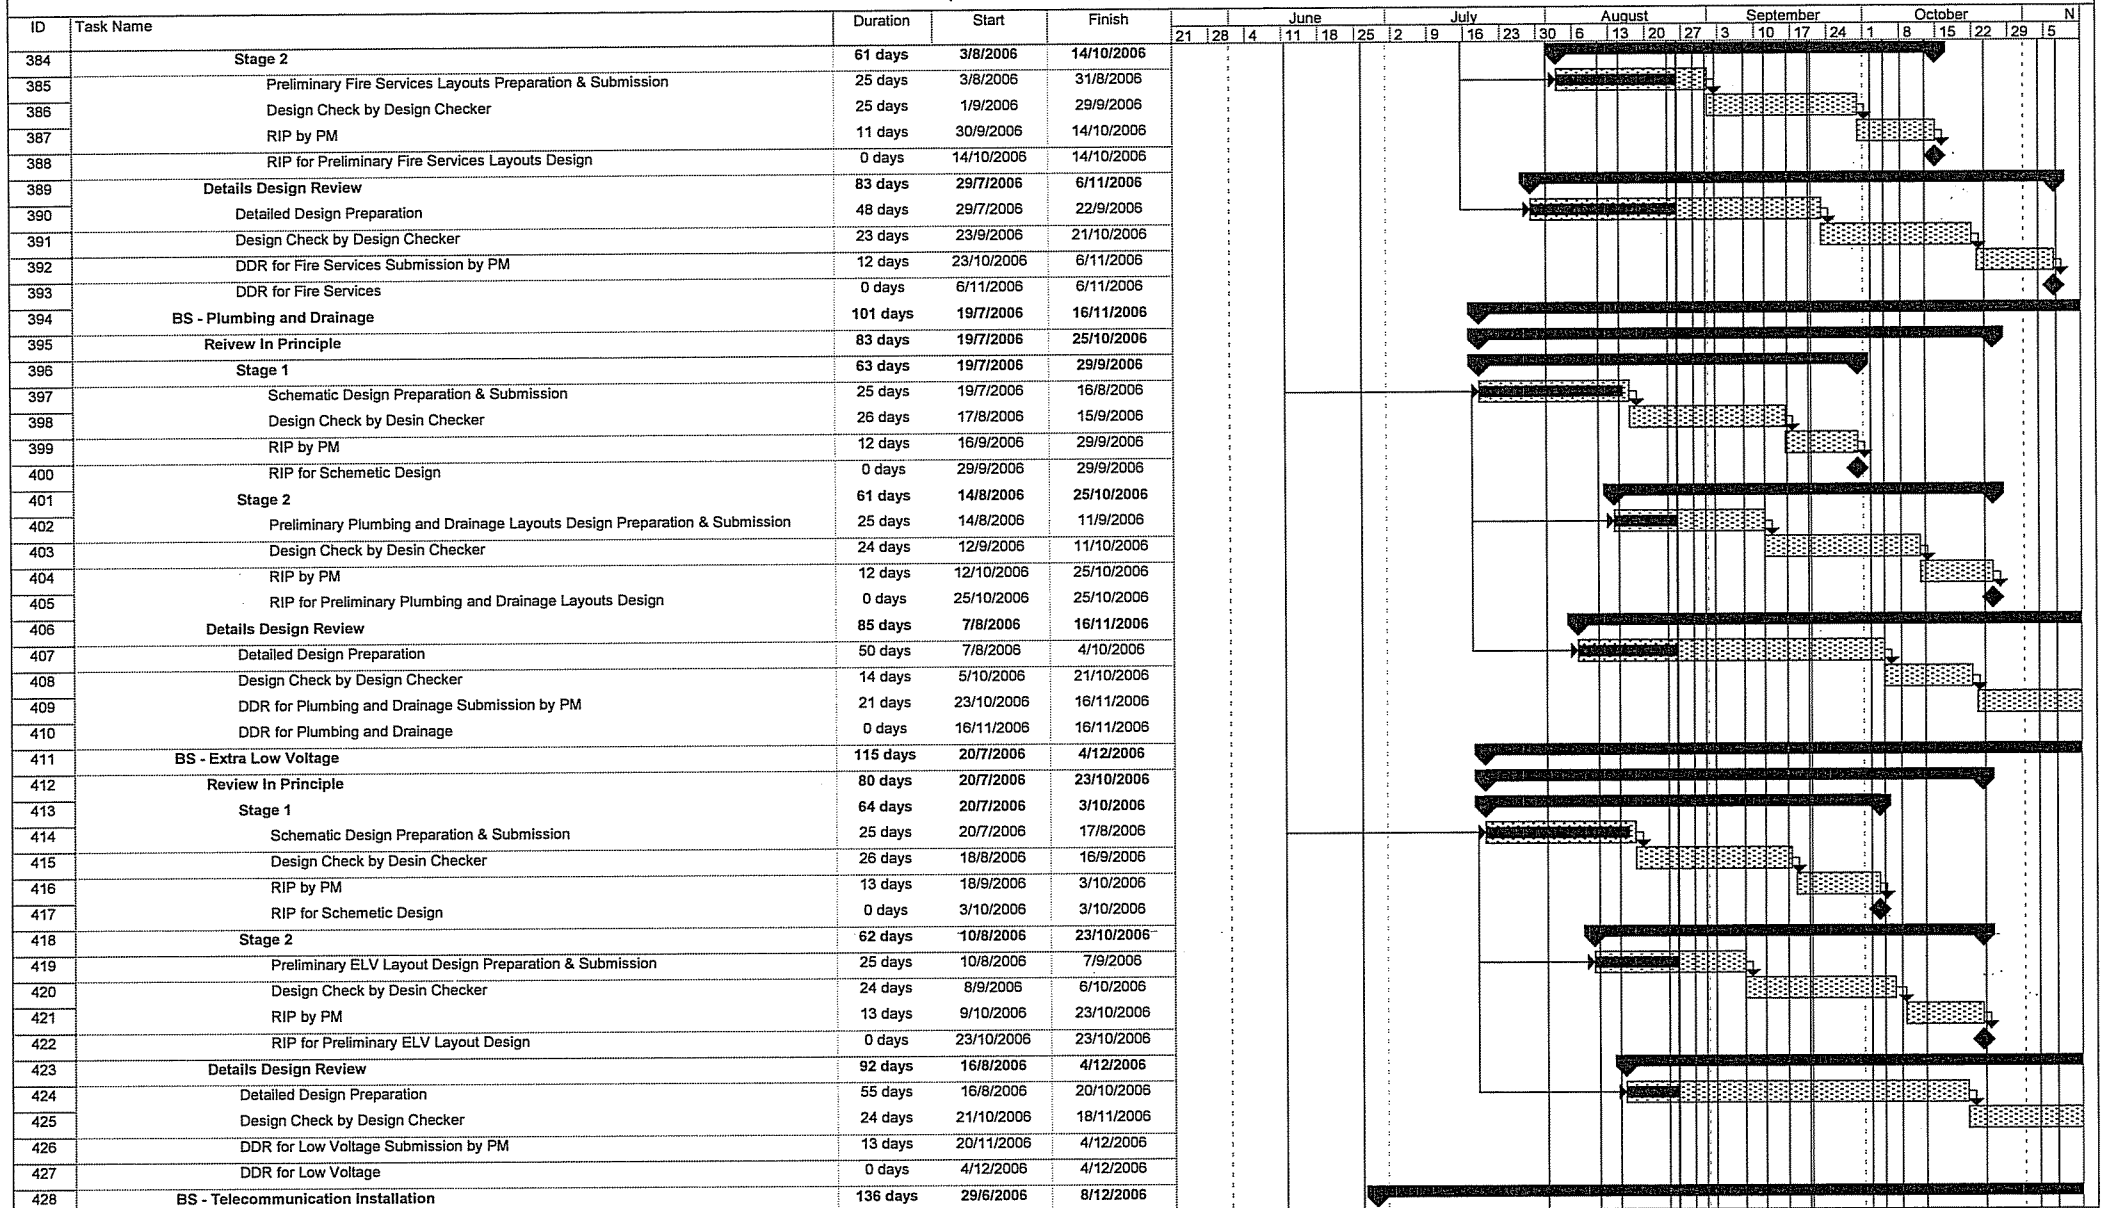


Project: 3 Months Rolling Programme
Date: 25/8/2006

Task
Progress
Milestone



Summary
Rolled Up Task
Rolled Up Milestone



Rolled Up Progress
Split
External Tasks



Project Summary
Group By Summary
Deadline



Hong Kong Convention and Exhibition Centre Expansion Project 3 Months Rolling Programme (2006-08-11 to 2006-11-10)																																
ID	Task Name	Duration	Start	Finish	Gantt Chart (June to October 2006)																											
429	Review In Principle	101 days	29/6/2006	27/10/2006	[Gantt Bar]																											
430	Stage 1	81 days	29/6/2006	3/10/2006	[Gantt Bar]																											
431	Schematic Design Preparation & Submission	42 days	29/6/2006	17/8/2006	[Gantt Bar]																											
432	Design Check by Design Checker	26 days	18/8/2006	16/9/2006	[Gantt Bar]																											
433	RIP by PM	13 days	18/9/2006	3/10/2006	[Gantt Bar]																											
434	RIP for Schematic Design	0 days	3/10/2006	3/10/2006	[Gantt Bar]																											
435	Stage 2	79 days	26/7/2006	27/10/2006	[Gantt Bar]																											
436	Preliminary IT System Layouts Design Preparation & Submission	42 days	26/7/2006	12/9/2006	[Gantt Bar]																											
437	Design Check by Design Checker	24 days	13/9/2006	12/10/2006	[Gantt Bar]																											
438	RIP by PM	13 days	13/10/2006	27/10/2006	[Gantt Bar]																											
439	RIP for Preliminary IT System Layouts Design	0 days	27/10/2006	27/10/2006	[Gantt Bar]																											
440	Details Design Review	115 days	25/7/2006	8/12/2006	[Gantt Bar]																											
441	Detailed Design Preparation	49 days	25/7/2006	24/10/2006	[Gantt Bar]																											
442	Design Check by Design Checker	26 days	25/10/2006	24/11/2006	[Gantt Bar]																											
443	DDR for Submission by PM	12 days	25/11/2006	8/12/2006	[Gantt Bar]																											
444	DDR for Telecommunication Plan	0 days	8/12/2006	8/12/2006	[Gantt Bar]																											
445	Procurement	565 days	2/6/2006	28/4/2008	[Gantt Bar]																											
446	Specialist Package	565 days	2/6/2006	28/4/2008	[Gantt Bar]																											
447	Heavy Lifting for Steel Roof Trusses	160 days	20/12/2006	10/7/2007	[Gantt Bar]																											
448	Slide Beam/Lifting Frame/Strand Jack/Temporary Works	160 days	20/12/2006	10/7/2007	[Gantt Bar]																											
449	Procure Materials for Heavy Lifting System	100 days	20/12/2006	26/4/2007	[Gantt Bar]																											
450	Procure Materials for Slide Beams & Tie Beams	100 days	20/12/2006	26/4/2007	[Gantt Bar]																											
452	Concrete For Construction	533 days	11/7/2006	28/4/2008	[Gantt Bar]																											
453	Foundation	60 days	11/7/2006	18/9/2006	[Gantt Bar]																											
454	Design Mix Preparation & Submission	6 days	11/7/2006	17/7/2006	[Gantt Bar]																											
456	Check by Design Checker	12 days	22/7/2006	4/8/2006	[Gantt Bar]																											
457	Trial Mix Report Preparation & Submission	35 days	2/8/2006	1/9/2006	[Gantt Bar]																											
458	Design Check by Design Checker	3 days	12/9/2006	14/9/2006	[Gantt Bar]																											
459	Review by PM	3 days	15/9/2006	18/9/2006	[Gantt Bar]																											
460	Superstructure	41 days	19/9/2006	8/11/2006	[Gantt Bar]																											
461	Design Mix Preparation & Submission	6 days	19/9/2006	25/9/2006	[Gantt Bar]																											
462	Design Check by Design Checker	3 days	26/9/2006	28/9/2006	[Gantt Bar]																											
463	Trial Mix Report Preparation & Submission	26 days	4/10/2006	4/11/2006	[Gantt Bar]																											
464	Review by PM	3 days	6/11/2006	8/11/2006	[Gantt Bar]																											
467	Pontoons for Construction Works	50 days	15/9/2006	15/11/2006	[Gantt Bar]																											
468	Submission to Marine Department	0 days	22/9/2006	22/9/2006	[Gantt Bar]																											
469	Review By Marine Department	30 days	23/9/2006	31/10/2006	[Gantt Bar]																											
470	Approval by Marine Department	0 days	31/10/2006	31/10/2006	[Gantt Bar]																											
471	Material Procurement & Delivery	38 days	15/9/2006	1/11/2006	[Gantt Bar]																											
472	Commencement to assemble on Site	0 days	1/11/2006	1/11/2006	[Gantt Bar]																											
473	Assemble Pontoon on Site	12 days	2/11/2006	15/11/2006	[Gantt Bar]																											
474	Steel Piles	79 days	29/6/2006	29/9/2006	[Gantt Bar]																											
475	Procure Materials & Delivery to Site (Marine Pile)	25 days	1/9/2006	29/9/2006	[Gantt Bar]																											
476	Procure Materials & Delivery to Site (Pre-bored H Pile)	25 days	29/6/2006	28/7/2006	[Gantt Bar]																											
477	Structural Steel Works	420 days	2/6/2006	29/10/2007	[Gantt Bar]																											

Project: 3 Months Rolling Programme
Date: 25/8/2006

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary

Deadline

Page 8

Hong Kong Convention and Exhibition Centre
Expansion Project
3 Months Rolling Programme
(2006-08-11 to 2006-11-10)


ID	Task Name	Duration	Start	Finish	June							July				August				September				October					N	
					21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29		5
483	Shop Drawing Submission & Approval	45 days	18/9/2006	11/11/2006																										
484	Structural Steel Supplier Review by PM	6 days	18/9/2006	23/9/2006																										
485	First Delivery to Fabrication Yards	0 days	1/11/2006	1/11/2006																										
486	Fabrication of Structural Steel Works	284 days	13/11/2006	29/10/2007																										
488	Others Structural Works	90 days	4/11/2006	23/2/2007																										
489	Procure Movement Joint	90 days	4/11/2006	23/2/2007																										
498	M & E Long - Lead Items	319 days	21/10/2006	17/11/2007																										
501	Lift & Escalator Procurement & Delivery	180 days	21/10/2006	2/6/2007																										
506	Bearing for Steel Truss	92 days	18/9/2006	9/1/2007																										
507	Shop Drawing Submission & Approval	14 days	18/9/2006	4/10/2006																										
508	Bearing Procurement and Delivery	78 days	5/10/2006	9/1/2007																										
509	Contractor Submission	651 days	15/5/2006	24/7/2008																										
544	Site Mobilisation	38 days	7/7/2006	19/8/2006																										
545	Site Office Set Up	38 days	7/7/2006	19/8/2006																										
546	Site Office Set Up	38 days	7/7/2006	19/8/2006																										
558	Internal Hoarding Erection at Existing Atrium Link	124 days	1/8/2006	28/12/2006																										
559	For West Façade Removal and Structural Modification Beside Existing West Façade Truss	112 days	1/8/2006	12/12/2006																										
560	Bamboo Scaffolding Erection (Stage 1)	19 days	1/8/2006	23/8/2006																										
561	Hoarding Erection	24 days	23/8/2006	19/9/2006																										
562	Bamboo Scaffolding Erection (Stage 2)	6 days	8/11/2006	15/11/2006																										
563	Hoarding Erection	24 days	15/11/2006	12/12/2006																										
564	For GL 17/A&B Columns Construction	49 days	31/10/2006	28/12/2006																										
565	Bamboo Scaffolding Erection	12 days	31/10/2006	13/11/2006																										
566	Hoarding Erection	45 days	4/11/2006	28/12/2006																										
567	A & A Works to Existing HKCEC Phase 1 and 2	649 days	19/7/2006	24/9/2008																										
602	A & A Works to HKCEC Phase 2	647 days	19/7/2006	22/9/2008																										
603	HKCEC Phase 2 - Demolition Works (GL 16/B-E)	143 days	19/7/2006	8/1/2007																										
604	Condition Suvey for Affected Area	6 days	19/7/2006	26/7/2006																										
605	Erect Weather Proof Hoarding / Protective measure	32 days	26/7/2006	31/8/2006																										
606	Remove Existing Finishes & Feature	21 days	1/9/2006	25/9/2006																										
607	Modification for Existing E&M Services	44 days	11/8/2006	30/9/2006																										
608	Modification/Remove for External Facade	28 days	1/9/2006	4/10/2006																										
609	Demolition of Structure for Grid 16/B-E	45 days	5/10/2006	28/11/2006																										
610	Make Good for Existing Structure / finishing works	14 days	29/11/2006	14/12/2006																										
621	Modification of Existing Atrium Link	303 days	13/12/2006	20/12/2007																										
622	Demolition of Existing West Glass Wall at Atrium Link	35 days	13/12/2006	25/1/2007																										
623	Demolition of Existing West Glass Wall	35 days	13/12/2006	25/1/2007																										
641	New Atrium Link Extension	802 days	27/6/2006	11/3/2009																										
642	Material Handling Facilities & Temporary Working Platforms	196 days	30/9/2006	2/6/2007																										
643	Temporary Steel Working Platform (for Roof Trusses Assemble)	64 days	30/9/2006	16/12/2006																										
644	Maine Pile Construction	55 days	30/9/2006	6/12/2006																										
645	On Site fabrication of Bracing	55 days	5/10/2006	9/12/2006																										
646	On Site fabrication of Supports	55 days	10/10/2006	13/12/2006																										
647	Temporary Working Platform Erection	55 days	13/10/2006	16/12/2006																										
648	Commencement for Roof Truss Erection	0 days	16/12/2006	16/12/2006																										

Project: 3 Months Rolling Programme
Date: 25/8/2006

Task
Progress
Milestone




Summary
Rolled Up Task
Rolled Up Milestone



Rolled Up Progress
Split
External Tasks



Project Summary
Group By Summary
Deadline



Hong Kong Convention and Exhibition Centre
Expansion Project
3 Months Rolling Programme
(2006-08-11 to 2006-11-10)

ID	Task Name	Duration	Start	Finish
649	Temporary Steel Working Platform (for A1 Panel Truss Assemble)	39 days	16/11/2006	3/1/2007
651	On Site fabrication of Bracing	30 days	20/11/2006	23/12/2006
652	On Site fabrication of Supports	30 days	23/11/2006	29/12/2006
653	Temporary Working Platform Erection	30 days	27/11/2006	3/1/2007
654	Commencement for Panel Truss Erection	0 days	3/1/2007	3/1/2007
658	Piling and Sub-Structure	251 days	27/6/2006	2/5/2007
659	Pre-drilling Works	67 days	27/6/2006	13/9/2006
660	Pre-drilling Work with Armour Rock Coring (South except work area E)	40 days	18/7/2006	1/9/2006
661	Pre-drilling Work without Armour Rock Coring (North)	51 days	27/6/2006	25/8/2006
662	Pre-drilling Work with Armour Rock Coring for Work Area E	31 days	1/8/2006	5/9/2006
663	Pre-drilling Report Submission (South except work area E)	0 days	9/9/2006	9/9/2006
664	Pre-drilling Report Submission (North)	0 days	2/8/2006	2/8/2006
665	Pre-drilling Report Submission for Work Area E	0 days	13/9/2006	13/9/2006
666	Piling Works at North	198 days	1/8/2006	2/4/2007
667	Prebored H Piles Construction (Grid 16/A1, 17/A, B & E)	118 days	1/8/2006	19/12/2006
668	Remove Existing Pavement	12 days	1/8/2006	15/8/2006
669	Mobilization	12 days	1/8/2006	14/8/2006
670	Prebored H Piles Construction (Grid 16/A1, 17/ A, B & E)	70 days	15/8/2006	7/11/2006
671	Prebored H Piling for Temp. Access Platform	12 days	8/11/2006	21/11/2006
672	Submit Pile Record Plan to Consultant	6 days	8/11/2006	14/11/2006
673	Report Completion to PM	0 days	14/11/2006	14/11/2006
674	PM Select Pile for Testing	6 days	15/11/2006	21/11/2006
675	Loading Test for Selected Pile	18 days	22/11/2006	12/12/2006
676	Consent for Pile Cap & Structure Works	6 days	13/12/2006	19/12/2006
677	Prebored H Piles Construction (Grid 17/ B, C & D)	198 days	1/8/2006	2/4/2007
678	Remove Existing Pavement	12 days	1/8/2006	15/8/2006
679	Mobilization	12 days	1/8/2006	14/8/2006
680	Prebored H Piles Construction (Grid 17/ B, C & D)	150 days	15/8/2006	15/2/2007
686	Piling Works at South	162 days	2/8/2006	16/2/2007
687	Foundation Works for Grid A1 and A	103 days	2/8/2006	2/12/2006
688	For Grid A1 Prebored H Pile (A1/24)	103 days	2/8/2006	2/12/2006
689	Remove Existing Pavement for grid A1	14 days	2/8/2006	18/8/2006
690	Precautional & Protective Measure for U/G Serv.	10 days	22/8/2006	2/9/2006
691	Prebored Piles Construction	40 days	2/9/2006	20/10/2006
692	Submit Pile Record Plan to Consultant	6 days	21/10/2006	27/10/2006
693	PM Select Pile for Testing	6 days	28/10/2006	4/11/2006
694	Loading Test for Selected Pile	18 days	6/11/2006	25/11/2006
695	Consent for Pile Cap & Structure Works	6 days	27/11/2006	2/12/2006
696	Foundation Works for Grid A, B, C & D (BP2, BP3, BP4 & BP5)	144 days	23/8/2006	16/2/2007
697	Remove Existing Pavement for Grid B-D	23 days	14/9/2006	13/10/2006
698	Precautional & Protective Measure for U/G Serv.	12 days	23/8/2006	6/9/2006
699	Temporary steel platform / Equipment Fabrication	30 days	6/9/2006	12/10/2006
700	Bored Piles Construction (Grid 24/ B, C and D)	75 days	13/10/2006	12/1/2007

Project: 3 Months Rolling Programme
Date: 25/8/2006

2013年12月15日

卷之四

المؤمنين الذين آمنوا وهم يقاتلون في سبيل الله فيكون لهم من الله أجر عظيم

• • • • •

1998, 1999, 2000, 2001, 2002, 2003, 2004, 2005, 2006, 2007, 2008, 2009, 2010, 2011, 2012, 2013, 2014, 2015, 2016, 2017, 2018, 2019, 2020, 2021, 2022, 2023, 2024, 2025, 2026, 2027, 2028, 2029, 2030, 2031, 2032, 2033, 2034, 2035, 2036, 2037, 2038, 2039, 2040, 2041, 2042, 2043, 2044, 2045, 2046, 2047, 2048, 2049, 2050, 2051, 2052, 2053, 2054, 2055, 2056, 2057, 2058, 2059, 2060, 2061, 2062, 2063, 2064, 2065, 2066, 2067, 2068, 2069, 2070, 2071, 2072, 2073, 2074, 2075, 2076, 2077, 2078, 2079, 2080, 2081, 2082, 2083, 2084, 2085, 2086, 2087, 2088, 2089, 2090, 2091, 2092, 2093, 2094, 2095, 2096, 2097, 2098, 2099, 2100, 2101, 2102, 2103, 2104, 2105, 2106, 2107, 2108, 2109, 2110, 2111, 2112, 2113, 2114, 2115, 2116, 2117, 2118, 2119, 2120, 2121, 2122, 2123, 2124, 2125, 2126, 2127, 2128, 2129, 2130, 2131, 2132, 2133, 2134, 2135, 2136, 2137, 2138, 2139, 2140, 2141, 2142, 2143, 2144, 2145, 2146, 2147, 2148, 2149, 2150, 2151, 2152, 2153, 2154, 2155, 2156, 2157, 2158, 2159, 2160, 2161, 2162, 2163, 2164, 2165, 2166, 2167, 2168, 2169, 2170, 2171, 2172, 2173, 2174, 2175, 2176, 2177, 2178, 2179, 2180, 2181, 2182, 2183, 2184, 2185, 2186, 2187, 2188, 2189, 2190, 2191, 2192, 2193, 2194, 2195, 2196, 2197, 2198, 2199, 2200, 2201, 2202, 2203, 2204, 2205, 2206, 2207, 2208, 2209, 2210, 2211, 2212, 2213, 2214, 2215, 2216, 2217, 2218, 2219, 2220, 2221, 2222, 2223, 2224, 2225, 2226, 2227, 2228, 2229, 2230, 2231, 2232, 2233, 2234, 2235, 2236, 2237, 2238, 2239, 2240, 2241, 2242, 2243, 2244, 2245, 2246, 2247, 2248, 2249, 2250, 2251, 2252, 2253, 2254, 2255, 2256, 2257, 2258, 2259, 2260, 2261, 2262, 2263, 2264, 2265, 2266, 2267, 2268, 2269, 2270, 2271, 2272, 2273, 2274, 2275, 2276, 2277, 2278, 2279, 2280, 2281, 2282, 2283, 2284, 2285, 2286, 2287, 2288, 2289, 2290, 2291, 2292, 2293, 2294, 2295, 2296, 2297, 2298, 2299, 2300, 2301, 2302, 2303, 2304, 2305, 2306, 2307, 2308, 2309, 2310, 2311, 2312, 2313, 2314, 2315, 2316, 2317, 2318, 2319, 2320, 2321, 2322, 2323, 2324, 2325, 2326, 2327, 2328, 2329, 2330, 2331, 2332, 2333, 2334, 2335, 2336, 2337, 2338, 2339, 2340, 2341, 2342, 2343, 2344, 2345, 2346, 2347, 2348, 2349, 2350, 2351, 2352, 2353, 2354, 2355, 2356, 2357, 2358, 2359, 2360, 2361, 2362, 2363, 2364, 2365, 2366, 2367, 2368, 2369, 2370, 2371, 2372, 2373, 2374, 2375, 2376, 2377, 2378, 2379, 2380, 2381, 2382, 2383, 2384, 2385, 2386, 2387, 2388, 2389, 2390, 2391, 2392, 2393, 2394, 2395, 2396, 2397, 2398, 2399, 2400, 2401, 2402, 2403, 2404, 2405, 2406, 2407, 2408, 2409, 2410, 2411, 2412, 2413, 2414, 2415, 2416, 2417, 2418, 2419, 2420, 2421, 2422, 2423, 2424, 2425, 2426, 2427, 2428, 2429, 2430, 2431, 2432, 2433, 2434, 2435, 2436, 2437, 2438, 2439, 2440, 2441, 2442, 2443, 2444, 2445, 2446, 2447, 2448, 2449, 2450, 2451, 2452, 2453, 2454, 2455, 2456, 2457, 2458, 2459, 2460, 2461, 2462, 2463, 2464, 2465, 2466, 2467, 2468, 2469, 2470, 2471, 2472, 2473, 2474, 2475, 2476, 2477, 2478, 2479, 2480, 2481, 2482, 2483, 2484, 2485, 2486, 2487, 2488, 2489, 2490, 2491, 2492, 2493, 2494, 2495, 2496, 2497, 2498, 2499, 2500, 2501, 2502, 2503, 2504, 2505, 2506, 2507, 2508, 2509, 2510, 2511, 2512, 2513, 2514, 2515, 2516, 2517, 2518, 2519, 2520, 2521, 2522, 2523, 2524, 2525, 2526, 2527, 2528, 2529, 2530, 2531, 2532, 2533, 2534, 2535, 2536, 2537, 2538, 2539, 2540, 2541, 2542, 2543, 2544, 2545, 2546, 2547, 2548, 2549, 2550, 2551, 2552, 2553, 2554, 2555, 2556, 2557, 2558, 2559, 2560, 2561, 2562, 2563, 2564, 2565, 2566, 2567, 2568, 2569, 2570, 2571, 2572, 2573, 2574, 2575, 2576, 2577, 2578, 2579, 2580, 2581, 2582, 2583, 2584, 2585, 2586, 2587, 2588, 2589, 2590, 2591, 2592, 2593, 2594, 2595, 2596, 2597, 2598, 2599, 2600, 2601, 2602, 2603, 2604, 2605, 2606, 2607, 2608, 2609, 2610, 2611, 2612, 2613, 2614, 2615, 2616, 2617, 2618, 2619, 2620, 2621, 2622, 2623, 2624, 2625, 2626, 2627, 2628, 2629, 2630, 2631, 2632, 2633, 2634, 2635, 2636, 2637, 2638, 2639, 2640, 2641, 2642, 2643, 2644, 2645, 2646, 2647, 2648, 2649, 2650, 2651, 2652, 2653, 2654, 2655, 2656, 2657, 2658, 2659, 2660, 2661, 2662, 2663, 2664, 2665, 2666, 2667, 2668, 2669, 2670, 2671, 2672, 2673, 2674, 2675, 2676, 2677, 2678, 2679, 26

234-235-236-237-238-239-240-241-242-243-244-245-246-247-248-249-250-251-252-253-254-255-256-257-258-259-260-261-262-263-264-265-266-267-268-269-270-271-272-273-274-275-276-277-278-279-280-281-282-283-284-285-286-287-288-289-290-291-292-293-294-295-296-297-298-299-300-301-302-303-304-305-306-307-308-309-310-311-312-313-314-315-316-317-318-319-320-321-322-323-324-325-326-327-328-329-330-331-332-333-334-335-336-337-338-339-340-341-342-343-344-345-346-347-348-349-350-351-352-353-354-355-356-357-358-359-360-361-362-363-364-365-366-367-368-369-370-371-372-373-374-375-376-377-378-379-380-381-382-383-384-385-386-387-388-389-390-391-392-393-394-395-396-397-398-399-400-401-402-403-404-405-406-407-408-409-410-411-412-413-414-415-416-417-418-419-420-421-422-423-424-425-426-427-428-429-430-431-432-433-434-435-436-437-438-439-440-441-442-443-444-445-446-447-448-449-450-451-452-453-454-455-456-457-458-459-460-461-462-463-464-465-466-467-468-469-470-471-472-473-474-475-476-477-478-479-480-481-482-483-484-485-486-487-488-489-490-491-492-493-494-495-496-497-498-499-500-501-502-503-504-505-506-507-508-509-510-511-512-513-514-515-516-517-518-519-520-521-522-523-524-525-526-527-528-529-530-531-532-533-534-535-536-537-538-539-540-541-542-543-544-545-546-547-548-549-550-551-552-553-554-555-556-557-558-559-560-561-562-563-564-565-566-567-568-569-570-571-572-573-574-575-576-577-578-579-580-581-582-583-584-585-586-587-588-589-590-591-592-593-594-595-596-597-598-599-600-601-602-603-604-605-606-607-608-609-610-611-612-613-614-615-616-617-618-619-620-621-622-623-624-625-626-627-628-629-630-631-632-633-634-635-636-637-638-639-640-641-642-643-644-645-646-647-648-649-650-651-652-653-654-655-656-657-658-659-660-661-662-663-664-665-666-667-668-669-670-671-672-673-674-675-676-677-678-679-680-681-682-683-684-685-686-687-688-689-690-691-692-693-694-695-696-697-698-699-700-701-702-703-704-705-706-707-708-709-710-711-712-713-714-715-716-717-718-719-720-721-722-723-724-725-726-727-728-729-730-731-732-733-734-735-736-737-738-739-740-741-742-743-744-745-746-747-748-749-750-751-752-753-754-755-756-757-758-759-760-761-762-763-764-765-766-767-768-769-770-771-772-773-774-775-776-777-778-779-780-781-782-783-784-785-786-787-788-789-790-791-792-793-794-795-796-797-798-799-800-801-802-803-804-805-806-807-808-809-810-811-812-813-814-815-816-817-818-819-820-821-822-823-824-825-826-827-828-829-830-831-832-833-834-835-836-837-838-839-840-841-842-843-844-845-846-847-848-849-850-851-852-853-854-855-856-857-858-859-860-861-862-863-864-865-866-867-868-869-870-871-872-873-874-875-876-877-878-879-880-881-882-883-884-885-886-887-888-889-890-891-892-893-894-895-896-897-898-899-900-901-902-903-904-905-906-907-908-909-910-911-912-913-914-915-916-917-918-919-920-921-922-923-924-925-926-927-928-929-930-931-932-933-934-935-936-937-938-939-940-941-942-943-944-945-946-947-948-949-950-951-952-953-954-955-956-957-958-959-960-961-962-963-964-965-966-967-968-969-970-971-972-973-974-975-976-977-978-979-980-981-982-983-984-985-986-987-988-989-990-991-992-993-994-995-996-997-998-999-1000-1001-1002-1003-1004-1005-1006-1007-1008-1009-1010-1011-1012-1013-1014-1015-1016-1017-1018-1019-1020-1021-1022-1023-1024-1025-1026-1027-1028-1029-1030-1031-1032-1033-1034-1035-1036-1037-1038-1039-1040-1041-1042-1043-1044-1045-1046-1047-1048-1049-1050-1051-1052-1053-1054-1055-1056-1057-1058-1059-1060-1061-1062-1063-1064-1065-1066-1067-1068-1069-1070-1071-1072-1073-1074-1075-1076-1077-1078-1079-1080-1081-1082-1083-1084-1085-1086-1087-1088-1089-1090-1091-1092-1093-1094-1095-1096-1097-1098-1099-1100-1101-1102-1103-1104-1105-1106-1107-1108-1109-1110-1111-1112-1113-1114-1115-1116-1117-1118-1119-1120-1121-1122-1123-1124-1125-1126-1127-1128-1129-1130-1131-1132-1133-1134-1135-1136-1137-1138-1139-1140-1141-1142-1143-1144-1145-1146-1147-1148-1149-1150-1151-1152-1153-1154-1155-1156-1157-1158-1159-1160-1161-1162-1163-1164-1165-1166-1167-1168-1169-1170-1171-1172-1173-1174-1175-1176-1177-1178-1179-1180-1181-1182-1183-1184-1185-1186-1187-1188-1189-1190-1191-1192-1193-1194-1195-1196-1197-1198-1199-1200-1201-1202-1203-1204-1205-

