

# Jardine Engineering Corporation Limited

Contract No. DE/2009/09  
Supply and Installation of Electrical and  
Mechanical Equipment for Tai Po Sewage  
Treatment Works Stage 5 Phase 2B

## Monthly Environmental Monitoring and Audit Report for September 2014

(Version 2.0)

Certified By



(Environmental Team Leader)

### REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

### CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong  
Tel: (852) 2151 2083 Fax: (852) 3107 1388  
Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)

## TABLE OF CONTENTS

	Page
<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
Introduction .....	1
Environmental Monitoring and Audit Works .....	1
Environmental Licenses and Permits .....	1
Key Information in the Reporting Month.....	1
Future Key Issues .....	3
<b>1 INTRODUCTION .....</b>	<b>4</b>
Background .....	4
Construction Programme.....	6
Summary of EM&A Requirements .....	6
<b>2 AIR QUALITY MONITORING .....</b>	<b>8</b>
Monitoring Requirements.....	8
Monitoring Locations .....	8
Monitoring Equipment .....	8
Monitoring Parameters, Frequency and Duration .....	8
Monitoring Methodology and QA/QC Procedure.....	9
Results and Observations .....	10
<b>3 NOISE MONITORING .....</b>	<b>12</b>
Monitoring Requirements.....	12
Monitoring Locations .....	12
Monitoring Equipment .....	12
Monitoring Parameters, Frequency and Duration .....	12
Monitoring Methodology and QA/QC Procedures .....	13
Results and Observations .....	14
<b>4 ENVIRONMENTAL AUDIT.....</b>	<b>15</b>
Site Audits .....	15
Review of Environmental Monitoring Procedures.....	15
Status of Environmental Licensing and Permitting.....	15
Status of Waste Management .....	16
Implementation Status of Environmental Mitigation Measures.....	16
Summary of Exceedances .....	17
Implementation Status of Event Action Plans.....	17
Summary of Complaint and Prosecution.....	17
<b>5 FUTURE KEY ISSUES .....</b>	<b>18</b>
Monitoring Schedule for the Next Month .....	18
Construction Program for the Next Month.....	18
<b>6 CONCLUSIONS AND RECOMMENDATIONS .....</b>	<b>18</b>
Conclusions .....	19
Recommendations .....	19

## **LIST OF TABLES**

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 2.4	Summary Table of Air Quality Monitoring Results during the reporting month
Table 3.1	Location of Noise Monitoring Station
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Summary Table of Noise Monitoring Results during the Reporting Month
Table 4.1	Summary of Environmental Licensing and Permit Status
Table 4.2	Observations and Recommendations of Site Audit

## **LIST OF FIGURE**

Figure 1.1	Site Layout Plan
Figure 1.2	Locations of Air Quality and Noise Monitoring Stations

## **LIST OF APPENDICES**

Appendix A	Action and Limit Levels
Appendix B	Copies of Calibration Certificates
Appendix C	Environmental Monitoring Schedules
Appendix D	1-hour TSP Monitoring Results and Graphical Presentations
Appendix E	24-hour TSP Monitoring Results and Graphical Presentations
Appendix F	Noise Monitoring Results and Graphical Presentations
Appendix G	Summary of Exceedance
Appendix H	Site Audit Summary
Appendix I	Event Action Plans
Appendix J	Updated Environmental Mitigation Implementation Schedule
Appendix K	Waste Generation in the Reporting Month
Appendix L	Complaint Log
Appendix M	Construction Programme

**EXECUTIVE SUMMARY****Introduction**

1. This is the 39<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for DSD Contract no. DE/2009/09 “Supply and Installation of Electrical and Mechanical Equipment for Tai Po Sewage Treatment Works Stage 5 Phase 2B”. This report documents the findings of EM&A Works conducted in September 2014.
2. The major site activities undertaken in the reporting month included:
  - E&M installation of FC No.7B to 10B
  - Pipework installation for Flowmeter Chamber FMC2B
  - Migration work of existing equipment to new MCC3 at Stage IV RAS Pumping Station
  - T&C for E&M installation at Aeration Tank No.5, 6 & 7
  - Pipework installation for existing Air Blower No.3 and No.4
  - Migration work of existing equipment to new MCC2 at 1/F CBC
  - Commissioning of new Centrifuge No.4 for Sludge Thickening System
  - Installation of Screw Pump No.4 at Stage IV Inlet Works
  - E&M installation for new Sludge Digestion Tank No.3
  - BS & FS installation for various areas

**Environmental Monitoring and Audit Works**

3. Environmental monitoring and audit works for the Project were performed regularly as stipulated in the Final EM&A Manual and the results were checked and reviewed. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
4. Summary of the events and action taken in the reporting month is tabulated in **Table I**.

**Table I Summary Table for Events Recorded in the Reporting Month**

Parameter	No. of Exceedance		No. of Events Due to this Project	Action Taken
	Action Level	Limit Level		
1-hr TSP	0	0	0	N/A
24-hr TSP	0	0	0	N/A
Noise	0	0	0	N/A

**Environmental Licenses and Permits**

5. Environmental related licenses/permits granted to the Project include the Environmental Permit (EP) for the Project.

**Key Information in the Reporting Month**

6. Summary of key information in this reporting month is tabulated in **Table II**.

**Table II      Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Report (August 2014)	Submitted to EPD on 29 <sup>th</sup> September 2014 (EP condition 6.6)	N/A	---
Notifications of any summons & prosecutions	0	---	N/A	N/A	---

### **Future Key Issues**

7. Major site activities for the coming two months will include:
  - E&M installation of FC No.7B to 10B
  - Replacement of RAS Pump No.1 at Stage IV RAS Pumping Station
  - Migration work of existing equipment to new MCC3 at Stage IV RAS Pumping Station
  - T&C for E&M installation at Aeration Tank No. 5, 6 & 7
  - T&C for E&M installation at new PST No.5
  - Pipework installation for existing Air Blower No.3 and No.4
  - Migration work of existing equipment to new MCC2 at 1/F CBC
  - Installation of Screw Pump No.4 at Stage IV Inlet Works
  - E&M installation for new Sludge Digestion Tank No.3
  - BS & FS installation for various areas
8. The future environmental concerns are air quality, noise impacts and waste management from construction works.

## 1 INTRODUCTION

### Background

- 1.1 Tai Po Sewage Treatment Works (TPSTW) is located within the Tai Po Industrial Estate. It currently comprises four Stages: I, II, IVA and IVB works. The TPSTW - Stage V aims to upgrade the existing STW to provide additional sewage treatment capacity from the present design flow of 88,000 m<sup>3</sup>/day to 130,000 m<sup>3</sup>/day to meet the demands of both the existing and future developments, and to meet the revised discharge license requirements.
- 1.2 The TPSTW Stage V, Phase I and Phase II are Designated Projects under the Environmental Impact Assessment Ordinance (Cap. 449) with the same EIAO Register No. AEIAR – 081/2004. A study of environmental impact assessment (EIA) was undertaken to evaluate various environmental impacts associated with the works within these two Designed Projects. An EIA Report as well as an Environmental Monitoring and Audit (EM&A) Manual were approved by the Environmental Protection Department (EPD) on 28 October 2004.
- 1.3 The Stage V works will be implemented in 2 phases. The design capacities of Phase I and Phase II works are 100,000 m<sup>3</sup>/d and 130,000 m<sup>3</sup>/d respectively. An Environmental Permit (EP) No. EP-265/2007 was issued on 22 March 2007 for the TPSTW Stage V Phase II to the Drainage Services Department (DSD) as the Permit Holder. The project “Tai Po Sewage Treatment Works – Stage V Phase IIB” formed part of the Phase II works, includes additional secondary treatment process units ( 1 primary clarifier; 3 bioreactors and 2 final clarifiers) in TPSTW for its future extended plant design capacity of 120,000 m<sup>3</sup>/day. A master construction programme of the Project is provided in **Appendix M**. A site layout plan is provided in **Figure 1.1**. The construction activities of the Project commenced on 16 May 2011.
- 1.4 Cinotech Consultants Ltd. was commissioned by the Contractor as the Environmental Team (ET) to undertake the EM&A works for the Project. Dr. Priscilla CHOY of Cinotech Consultants Ltd. was appointed as the ET Leader as per the Condition 2.1 of the EP. Ove Arup and Partners Hong Kong Limited was appointed as the IEC under Condition 2.2 of the EP. This is the 39<sup>th</sup> monthly EM&A report summarizing the EM&A works for the Project in September 2014.


## Project Organizations

1.5 Different parties with different levels of involvement in the project organization include:

- Project Proponent / Engineer's Representative (ER) – Drainage Services Department
- Environmental Team (ET) – Cinotech Consultants Ltd.
- Independent Environmental Checker (IEC) – Ove Arup and Partners Hong Kong Limited
- Contractor – Jardine Engineering Corporation Ltd.

1.6 The responsibilities of respective parties are detailed in Section 1.10 of the Final EM&A Manual of the Project.

1.7 The Project Organization during Construction Phase

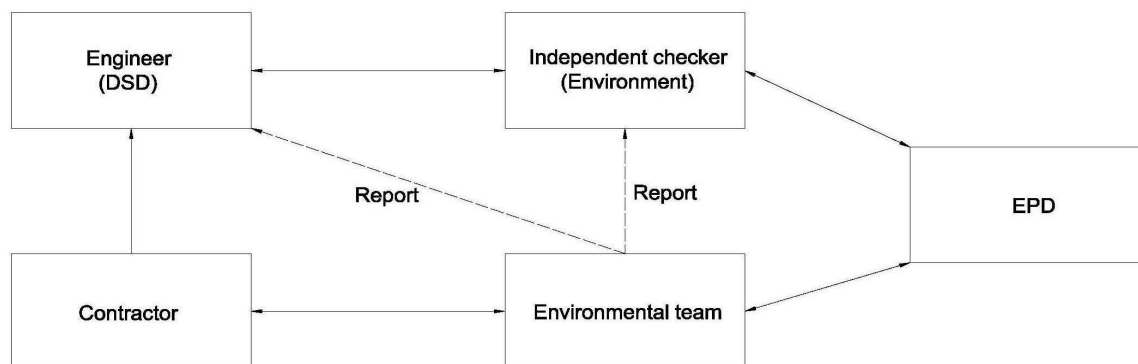

1.8 The key contacts of the Project are shown in **Table 1.1**.

**Table 1.1 Key Project Contacts**

Party	Role	Name	Position	Phone No.	Fax No.
DSD	E&M Branch	Mr. TONG Sau Kit	Senior Engineer	2594 7304	2827 8532
		Mr. TSE Ho	Engineer	2660 7638	
Cinotech	Environmental Team	Dr. Priscilla CHOY	ET Leader	2151 2089	3107 1388
		Mr. Harris Wong	Project Coordinator and Audit Team Leader	2151 2098	
		Mr. Henry LEUNG	Monitoring Team Leader	2151 2087	
Arup	Independent Environmental Checker	Mr. Coleman NG	Independent Environmental Checker	2268 3097	2865 6493
		Mr. Ken LEE	Assistant to Independent Environmental Checker	2268 3573	
JEC	E&M Contractor	Mr. Alex LAW	Project Manager	9312 8659	2887 9090
		Mr. Kim Hung LAU	Site Agent	6393 7548	
		Mr. Brendan CHAN	Environmental Officer	6892 0956	



## **Construction Programme**

1.9 The site activities undertaken in the reporting month were:

- E&M installation of FC No.7B to 10B
- Pipework installation for Flowmeter Chamber FMC2B
- Migration work of existing equipment to new MCC3 at Stage IV RAS Pumping Station
- T&C for E&M installation at Aeration Tank No.5, 6 & 7
- Pipework installation for existing Air Blower No.3 and No.4
- Migration work of existing equipment to new MCC2 at 1/F CBC
- Commissioning of new Centrifuge No.4 for Sludge Thickening System
- Installation of Screw Pump No.4 at Stage IV Inlet Works
- E&M installation for new Sludge Digestion Tank No.3
- BS & FS installation for various areas

### **Summary of EM&A Requirements**

- 1.10 The EM&A programme requires construction phase air quality and noise monitoring as well as environmental site audits. The EM&A requirements are described in the following sections, including:
- All monitoring parameters;
  - Action and Limit levels for all environmental parameters;
  - Event / Action Plans;
  - Environmental mitigation measures, as recommended in the project EIA study final report; and
  - Environmental requirements in contract documents.
- 1.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.
- 1.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely air quality and noise as well as audit works for the Project in the reporting month.

## 2 AIR QUALITY MONITORING

### Monitoring Requirements

- 2.1 Monitoring of 1-hour and 24-hour Total Suspended Particulates (TSP) was conducted to monitor the air quality during construction phase. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.
- 2.2 In accordance with Section 2.30 of the EM&A Manual, a baseline checking of ambient TSP levels shall be carried out every six months at each monitoring station, when no dusty works activities are in operation. The number and location of monitoring stations and parameters shall be reviewed by ET Leader every three months according to section 8.8 of EM&A Manual.

### Monitoring Locations

- 2.3 Impact air quality monitoring was conducted at the 3 monitoring stations, as shown in **Figure 1.2**. **Table 2.1** describes the locations of the air quality monitoring stations.

**Table 2.1 Locations for Air Quality Monitoring**

Monitoring Stations	Description	Location of Measurement
CAM1	Government Staff Quarters	Rooftop
CAM2	Hung Hing Printing Centre	On the site boundary just next to the Hung Hing Printing Centre
CAM3	Talcon Industrial Ltd.	On the site boundary just next to Talcon Industrial Ltd.

### Monitoring Equipment

- 2.4 **Table 2.2** summarizes the equipment used for the air quality monitoring.

**Table 2.2 Air Quality Monitoring Equipment**

Equipment	Model and Make	Qty.
HVS	Graseby GMW 2310 HVS, Model GS-2310105-1, Serial no. 10239 and 0810	2
	Tisch Environmental, Inc.; Model no. TE-5170, Serial no. 1704	1
Calibrator	TISCH.; Model no. TE-5025A Serial no. 0993	1

### Monitoring Parameters, Frequency and Duration

- 2.5 **Table 2.3** summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period.

**Table 2.3 Impact Dust Monitoring Parameters, Frequency and Duration**

Monitoring Stations	Parameter	Duration	Period	Frequency
CAM1, CAM2 and CAM3	1-hour TSP	1 hour	During daytime period	3 times / 6-day
	24-hour TSP	24 hours	24 hours	Once / 6-day

## Monitoring Methodology and QA/QC Procedure

### Instrumentation

- 2.6 High Volume Samplers (HVS) connected with appropriate sampling inlets were employed for air quality monitoring. Each sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

### HVS Installation

- 2.7 The following guidelines were adopted during the installation of HVS:
- Sufficient support was provided to secure the samplers against gusty wind.
  - No two samplers were placed less than 2 meters apart.
  - The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
  - A minimum of 2 meters of separation from walls, parapets and penthouses was required for rooftop samples.
  - A minimum of 2 meters separation from any supporting structure, measured horizontally was required.
  - No furnaces or incineration flues were nearby.
  - Airflow around the sampler was unrestricted.
  - The samplers were more than 20 meters from the drip line.
  - Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.

### Filters Preparation

- 2.8 Fiberglass filters were used which have a collection efficiency of larger than 99% for particles of 0.3  $\mu\text{m}$  diameter. A HOKLAS accredited laboratory, Wellab Ltd., was responsible for the preparation of pre-weighed filter papers for Cinotech's monitoring team.
- 2.9 All filters, which were prepared by Wellab Ltd., were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was < 50% and not variable by more than  $\pm 5\%$ . A convenient working RH was 40%.
- 2.10 Wellab Ltd. has a comprehensive quality assurance and quality control programmes.

## Operating/Analytical Procedures

2.11 Operating/analytical procedures for the TSP monitoring were highlighted as follows:

- Prior to the commencement of the dust sampling, the flow rate of the HVS was properly set (between 1.1 and 1.4 m<sup>3</sup>/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the air quality monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts to avoid air leakage at the edges.
- The shelter lid was closed and secured with the aluminum strip.
- The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- The flow rate of the HVS sampler would be verified to be constant and recorded on the data sheet after sampling.
- After sampling, the filter was removed and sent to the Wellab Ltd. for weighing. The elapsed time was also recorded.
- Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%. Weighing results were returned to Cinotech for further analysis of TSP concentrations collected by each filter.

## Maintenance/Calibration

2.12 The following maintenance/calibration was required for the HVS:

- The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
- Calibration of the HVS (five point calibration) using Calibration Kit was carried out every two months. Copies of calibration certificates are attached in **Appendix B**.
- The HVS calibration orifice will be calibrated annually.

## Results and Observations

2.13 In the reporting month, 1-hr TSP monitoring was carried out as schedule at each designated monitoring station on 14 occasions. 24-hr TSP monitoring was carried out as scheduled at each designated monitoring station on 6 occasions. The monitoring schedule was updated and is shown in **Appendix C**. The weather during the monitoring sessions was mainly sunny and fine.

2.14 All measured 1-hr and 24-hr TSP levels were below the Action/Limit Levels. No exceedance was recorded in the reporting month.

2.15 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in **Appendices D** and **E**, respectively.

**Table 2.4 Summary Table of Air Quality Monitoring Results during the reporting month**

Parameter	Minimum $\mu\text{g}/\text{m}^3$	Maximum $\mu\text{g}/\text{m}^3$	Average $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hr TSP (CAM1)	58	215	113	315	500
24-hr TSP (CAM1)	27	125	62	171	260
1-hr TSP (CAM2)	76	227	133	336	500
24-hr TSP (CAM2)	30	131	72	177	260
1-hr TSP (CAM3)	92	239	147	344	500
24-hr TSP (CAM3)	35	141	82	192	260

2.16 According to our field observations, the major dust source identified at the designated air quality monitoring stations are as follows:

Station	Major Pollution Source
CAM1 – Government Staff Quarters	Road Traffic Dust
CAM2 – Hung Hing Printing Centre	Road Traffic Dust and Excavation
CAM3 – Talcon Industrial Ltd.	Road Traffic Dust and Excavation

### 3 NOISE MONITORING

#### Monitoring Requirements

- 3.1 Noise monitoring was conducted in accordance with the EM&A Manual. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.
- 3.2 The number and location of monitoring stations and parameters shall be reviewed by ET Leader every three months according to section 8.8 of EM&A Manual.

#### Monitoring Locations

- 3.3 Noise monitoring was conducted at one designated monitoring station as presented in **Table 3.1**. **Figure 1.2** shows the locations of the monitoring station.

**Table 3.1 Location of Noise Monitoring Station**

Monitoring Station	Description	Location of Measurement
NM1	Government Staff Quarters	The corridor at the first floor.

#### Monitoring Equipment

- 3.4 **Table 3.2** summarizes the noise monitoring equipment model being used.

**Table 3.2 Noise Monitoring Equipment**

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	SVANTEK - SVAN 955, 957	3
Calibrator	SVANTEK – SV30A	2
Wind Speed Anemometer	Vane Anemometer, Model AZ8904 (Serial no. 974835)	1

#### Monitoring Parameters, Frequency and Duration

- 3.5 **Table 3.3** summarizes the monitoring parameters, frequency and total duration of monitoring.

**Table 3.3 Noise Monitoring Parameters, Frequency and Duration**

Station	Parameter	Period	Frequency
NM1	$L_{eq}(30 \text{ min.})$ ( $L_{10}$ and $L_{90}$ were also recorded as supplementary information)	0700-1900 hrs. on normal weekdays	Once a week

- 3.6 If construction works are extended to include works during the hours of 1900 - 0700, additional weekly impact monitoring would be carried out during evening and night-time works. Applicable permits under NCO have been obtained by the Contractor. The details of the Construction Noise Permit can be referred to **Table 5.1**.

## Monitoring Methodology and QA/QC Procedures

### Field Monitoring

3.7 The monitoring procedures are as follows:

- The microphone head of the sound level meter was positioned 1m exterior of the noise sensitive facade and lowered sufficiently so that the building's external wall acts as a reflecting surface.
- The battery condition was checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting : A
  - time weighting : Fast
  - measurement time : 30 minutes
- Prior to and after noise measurement, the meter was calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
- The wind speed at the monitoring station was checked with the portable wind meter. Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.
- Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- At the end of the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.

### Maintenance and Calibration

3.8 Maintenance and Calibration procedures were as follows:

- The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator were checked and calibrated at yearly intervals. Copies of calibration certificates are attached in **Appendix B**.



### Results and Observations

- 3.9 In the reporting month, noise monitoring during non-restricted hours was conducted as scheduled at the designated location on 5 occasions. As advised by the Contractor, no construction activities will be undertaken during restricted hours as such noise monitoring during restricted hours was omitted. The noise monitoring schedule is provided in **Appendix C**.
- 3.10 The details of the monitoring results and graphical presentations are shown in **Appendix F**. The weather during the monitoring sessions was mainly sunny and fine.
- 3.11 No Action/Limit Level exceedance for construction noise monitoring was recorded in the reporting month.

**Table 3.4 Summary Table of Noise Monitoring Results during the Reporting Month**

Parameter	Minimum Leq(30min) dB(A)	Maximum Leq(30min) dB(A)	Average Leq(30min) dB (A)	Action Level	Limit Level
NM1	58.4	68.2	64.0	When one documented complaint is received	75dB(A)

- 3.12 According to our field observations, the major noise source identified at the designated air quality monitoring stations are as follows:

Station	Major Noise Source
NM1 – Government Staff Quarters	Road Traffic Construction of Main Site

## 4 ENVIRONMENTAL AUDIT

### Site Audits

- 4.1 Site audits were carried out by ET on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix H**.
- 4.2 Site audits were conducted on 4<sup>th</sup>, 12<sup>th</sup>, 17<sup>th</sup>, 23<sup>rd</sup>, 29<sup>th</sup> September 2014 by ET. A joint site audit with the representative with ER, IEC, the Contractor and the ET was carried out on 12<sup>th</sup> September 2014. No site inspection was conducted by EPD during the reporting month. The details of observations during site audit can refer to **Table 4.2**.

### Review of Environmental Monitoring Procedures

- 4.3 The monitoring works conducted by the monitoring team were inspected regularly. The following observations have been recorded for the monitoring works:

#### *Air Quality Monitoring*

- The monitoring team recorded all observations around the monitoring stations within and outside the construction site.
- The monitoring team recorded the temperature and weather conditions on the monitoring days.

#### *Noise Monitoring*

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- Major noise sources were identified and recorded. Other intrusive noise attributing to the result was trimmed off by pausing the monitoring temporarily.

### Status of Environmental Licensing and Permitting

- 4.4 All permits/licenses obtained for the Project are summarized in **Table 4.1**.

**Table 4.1 Summary of Environmental Licensing and Permit Status**

Permit / License No.	Valid Period		Details	Status
	From	To		
Environmental Permit (EP)				
EP-265/2007	22/3/2007	N/A	<u>Expansion and upgrading of existing Tai Po Sewage Treatment Works from 100,000 m<sup>3</sup>/day to 130,000 m<sup>3</sup>/day:</u> (a) additional secondary treatment process units(1 primary clarified; 3 bioreactors and 2 final clarifiers); (b) reconstruction of 4 existing final clarified; (c) provision of ultraviolet disinfection facilities; (d) additional sludge treatment facilities; and (e) ancillary works to existing treatment facilities.	Valid
Registration of Chemical Waste Producer				
5517-727-T3270-01	--	N/A	Major chemical waste types: Spent lubricating oil, spend hydraulic oil, spend cooling oil, surplus paint, spent alkaline electrolyte, spent battery and battery parts containing heavy metals, scrap battery cell containing heavy metals, Nickel and its compounds, spent flammable liquid, spent copper etchant (Ferric chloride), Sodium hypochlorite, polymer, electric and torch bulbs and tubes, alkaline cleaner (spent alkaline solution)	Valid

**Status of Waste Management**

- 4.5 No Construction and Demolition (C&D) materials were generated in the reporting month. The quantities of waste generated in this reporting month are summarized in **Appendix K**.

**Implementation Status of Environmental Mitigation Measures**

- 4.6 According to the EIA Study Report, Environmental Permit and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the EMIS is provided in **Appendix J**.
- 4.7 During site inspections in the reporting month, no non-conformance was identified. In addition, there was no major environmental deficiency being identified on the site audit session on 17<sup>th</sup>, 23<sup>th</sup> and 29<sup>th</sup> September 2014. The observations and recommendations made during the audit sessions are summarized in **Table 4.2**.

**Table 4.2 Observations and Recommendations of Site Audit**

Parameters	Date	Observations and Recommendations	Follow-up
Water Quality	N/A	N/A	N/A
Air Quality	N/A	N/A	N/A
Noise	N/A	N/A	N/A
Waste/ Chemical Management	4 September 2014	<u>Reminder:</u> Plastic bottles should be sorted for recycling.	The item was observed improved/rectified by the Contractor during the audit session on 12 September 2014.
	4 September 2014	<u>Reminder:</u> Oil leaking from the control device at aeration tank should be cleared.	The item was observed improved/rectified by the Contractor during the audit session on 12 September 2014.
	12 September 2014	<u>Reminder:</u> Cardboards should be sorted for recycling.	The item was observed improved/rectified by the Contractor during the audit session on 17 September 2014.

**Summary of Exceedances**

- 4.8 No exceedance of monitoring results was recorded in the reporting month. Summary of exceedance is provided in **Appendix G**.

**Implementation Status of Event Action Plans**

- 4.9 The Event Action Plans for air quality and construction noise monitoring are presented in **Appendix I**. No exceedance was recorded and thus no action was required to be implemented.

**Summary of Complaint and Prosecution**

- 4.10 No environmental related complaint, prosecution or notification of summons was received in the reporting month.
- 4.11 There was no environmental complaint, prosecution or notification of summons received since the Project commencement. The Complaint Log is attached in **Appendix L**.

## 5 FUTURE KEY ISSUES

5.1 Key issues to be considered in the coming month include:

- C&D wastes generated from installation of E&M equipment;
- Apply good site practice during rainy season; and
- Accumulation of C&D waste and general waste on site.

### **Monitoring Schedule for the Next Month**

5.2 The tentative environmental monitoring schedule for the next month is shown in **Appendix C**.

### **Construction Program for the Next Month**

5.3 A tentative construction programme is provided in **Appendix M**. The major construction activities in the coming month will include:

- E&M installation of FC No.7B to 10B
- Replacement of RAS Pump No.1 at Stage IV RAS Pumping Station
- Migration work of existing equipment to new MCC3 at Stage IV RAS Pumping Station
- T&C for E&M installation at Aeration Tank No. 5, 6 & 7
- T&C for E&M installation at new PST No.5
- Pipework installation for existing Air Blower No.3 and No.4
- Migration work of existing equipment to new MCC2 at 1/F CBC
- Installation of Screw Pump No.4 at Stage IV Inlet Works
- E&M installation for new Sludge Digestion Tank No.3
- BS & FS installation for various areas

## **6 CONCLUSIONS AND RECOMMENDATIONS**

### **Conclusions**

- 6.1 Environmental monitoring and audit works were conducted in the reporting month. Site inspections were conducted on a weekly basis. The results were reviewed and checked.
- 6.2 No exceedance of monitoring results was recorded in the reporting month.
- 6.3 There was no environmental complaint, prosecution or notification of summons received.

### **Recommendations**

- 6.4 According to the environmental audit performed in the reporting month, the following recommendations were made:

#### ***Waste / Chemical Management***

- Good site practices should be adopted to check for any accumulation of waste materials on site and dispose waste materials at designated areas.
- Segregate and store different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.
- Equipments should be checked and maintained regularly to prevent oil leakage.


---

---

## FIGURES

---

---

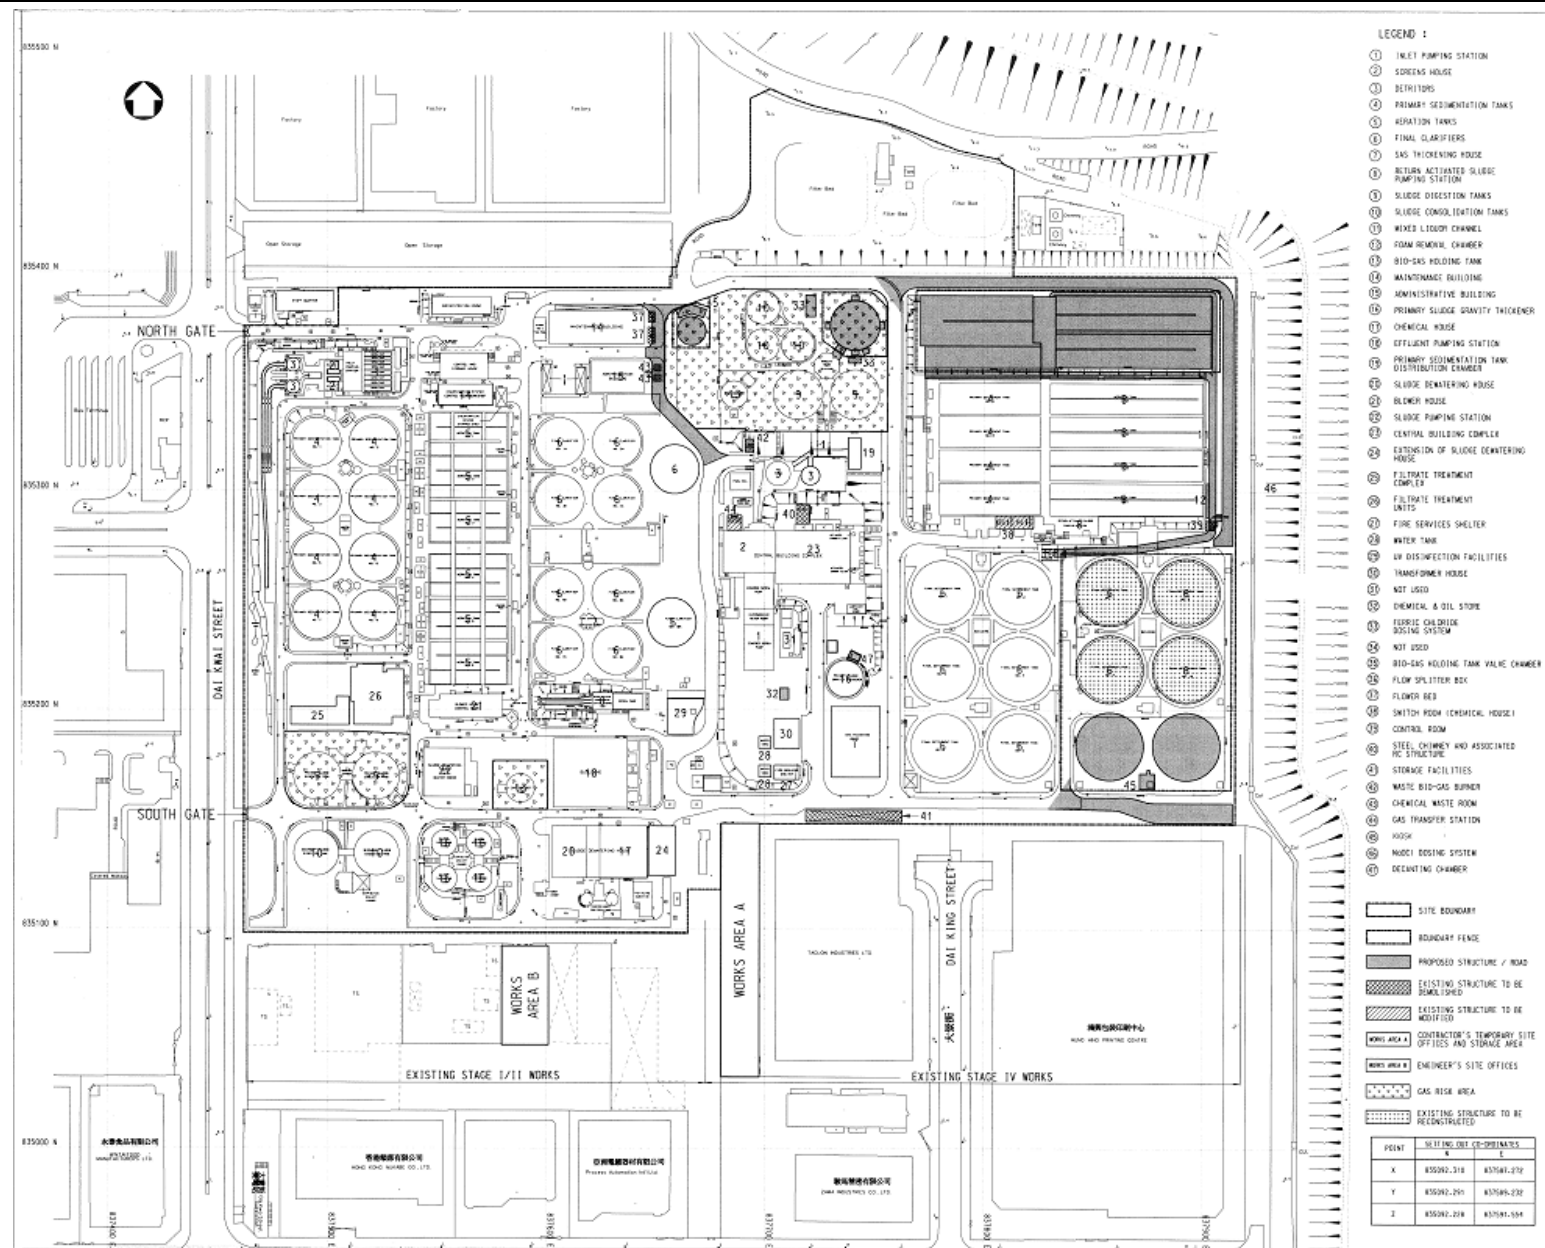

TAI PO SEWAGE TREATMENT WORKS, STAGE V, PHASE IIB

PROJECT SITE LAYOUT PLAN

Scale

N.T.S

Proposa

No.

MA10069

Date

Mar-11

Figure

1.1

CINOTECH





---

---

**APPENDIX A**  
**ACTION AND LIMIT LEVELS**

---

---

**APPENDIX A – Action and Limit Levels****1-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
CAM1	315	500
CAM2	336	
CAM3	344	

**24-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
CAM1	171	260
CAM2	177	
CAM3	192	

**Construction Noise**

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A)
0700-2300 hrs on holidays; and 1900-2300 hrs on all other days		70* dB(A)
2300-0700 hrs of next day		55* dB(A)

Notes:

\* The Area Sensitivity Rating for Station NM1 is taken as C, due to the nearby industrial area, according to Table 1 of EPD's Technical Memorandum on Noise from Construction Work other than Percussive Piling.

---

---

**APPENDIX B  
COPIES OF CALIBRATION  
CERTIFCATES**

---

---

# High-Volume TSP Sampler

## 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA0010/37/0058

Station CAM1 - Government Staff Quarter

Operator: WK

Date: 11-Aug-14

Next Due Date: 10-Oct-14

Equipment No.: A-01-37

Serial No. 1704

Ambient Condition			
Temperature, Ta (K)	300.3	Pressure, Pa (mmHg)	753.7

Orifice Transfer Standard Information					
Equipment No.:	A-04-04	Slope, mc	0.0588	Intercept, bc	-0.0461
Last Calibration Date:	30-Sep-13	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	29-Sep-14	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	11.9	3.42	58.98	8.0	2.81
2	9.4	3.04	52.51	6.4	2.51
3	7.6	2.73	47.29	5.1	2.24
4	5.4	2.31	39.99	3.3	1.80
5	3.3	1.80	31.43	2.0	1.40

By Linear Regression of Y on X

Slope, mw = 0.0519

Intercept, bw : -0.2397

Correlation coefficient\* = 0.9989

\*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation	
From the TSP Field Calibration Curve, take Qstd = 43 CFM	
From the Regression Equation, the "Y" value according to	
$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$	
Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ <u>4.04</u>	

Remarks: \_\_\_\_\_

Conducted by: Wk. Tang

Signature: Kwan

Date: 11/8/14

Checked by: Ar

Signature: \_\_\_\_\_

Date: 11 August 2014

# High-Volume TSP Sampler

## 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA0010/A40/0058

Station CAM2 - Hung Hing Printing Centre Operator: WK  
 Date: 11-Aug-14 Next Due Date: 10-Oct-14  
 Equipment No.: A-01-40 Serial No. 10239

Ambient Condition			
Temperature, Ta (K)	300.6	Pressure, Pa (mmHg)	753.4

Orifice Transfer Standard Information					
Equipment No.:	A-04-04	Slope, mc	0.0588	Intercept, bc	-0.0461
Last Calibration Date:	30-Sep-13	$mc \times Q_{std} + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	29-Sep-14	$Q_{std} = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	11.8	3.41	58.70	7.9	2.79
2	9.8	3.10	53.56	6.5	2.53
3	7.4	2.70	46.65	5.0	2.22
4	5.3	2.28	39.60	3.3	1.80
5	3.2	1.77	30.94	2.0	1.40

By Linear Regression of Y on X

Slope, mw = 0.0503 Intercept, bw = -0.1620  
 Correlation coefficient\* = 0.9992

\*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation	
From the TSP Field Calibration Curve, take Qstd = 43 CFM	
From the Regression Equation, the "Y" value according to	
$mw \times Q_{std} + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$	
Therefore, Set Point; $W = (mw \times Q_{std} + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ <u>4.08</u>	

Remarks: \_\_\_\_\_

Conducted by: Wk Tang Signature: Kwan Date: 11/8/14  
 Checked by: Gr Signature: \_\_\_\_\_ Date: 11 August 2014

# High-Volume TSP Sampler

## 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA0010/35/0058

Station CAM3 - Talcon Industrial Ltd

Operator: WK

Date: 11-Aug-14

Next Due Date: 10-Oct-14

Equipment No.: A-01-35

Serial No. 0810

Ambient Condition			
Temperature, Ta (K)	300.2	Pressure, Pa (mmHg)	753.8

Orifice Transfer Standard Information					
Equipment No.:	A-04-04	Slope, mc	0.0588	Intercept, bc	-0.0461
Last Calibration Date:	30-Sep-13	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	29-Sep-14	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	11.8	3.41	58.75	7.4	2.70
2	9.7	3.09	53.34	5.8	2.39
3	7.8	2.77	47.91	4.7	2.15
4	5.4	2.31	40.00	3.3	1.80
5	3.3	1.80	31.44	2.0	1.40

By Linear Regression of Y on X

Slope, mw = 0.0466

Intercept, bw = -0.0692

Correlation coefficient\* = 0.9991

\*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation	
From the TSP Field Calibration Curve, take Qstd = 43 CFM	
From the Regression Equation, the "Y" value according to	
$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$	
Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$	
	3.81

Remarks:

Conducted by: Wk Tang

Signature: Kwan

Date: 11/8/14

Checked by: Wk

Signature: [Signature]

Date: 11 August 2014

## TEST REPORT

Description Calibration Orifice  
Serial No. 0993  
Model No. TE-5025A  
Date 30 September 2013

Manufacturer TISCH  
Temperature, Ta (K) 300.8  
Pressure, Pa (mmHg) 759.3  
Equipment No.: A-04-04

Plate	Diff.Vol (m <sup>3</sup> )	Diff.Time (min)	Diff.Hg (mm)	Diff.H <sub>2</sub> O (in.)
1	1.00	1.4103	3.4	2.00
2	1.00	0.9980	6.8	4.00
3	1.00	0.8970	8.5	5.00
4	1.00	0.8540	9.4	5.50
5	1.00	0.7060	13.6	8.00

## DATA TABULATION

Vstd	(X axis) Qstd	(Y axis)
0.9853	0.6986	1.4069
0.9808	0.9828	1.9897
0.9786	1.0910	2.2245
0.9775	1.1446	2.3331
0.9720	1.3768	2.8138

Y axis=  $\text{SQRT}[\text{H}_2\text{O}(\text{Pa}/760)(298/\text{Ta})]$

Qstd Slope ( m ) = 2.07768

Intercept ( b ) = -0.04613

Coefficient ( r ) = 0.99997

Va	(X axis) Qa	(Y axis)
0.9955	0.7059	0.8901
0.9910	0.9930	1.2589
0.9888	1.1023	1.4074
0.9876	1.1565	1.4761
0.9821	1.3911	1.7803

Y axis=  $\text{SQRT}[\text{H}_2\text{O}(\text{Ta}/\text{Pa})]$

Qa Slope ( m ) = 1.30101

Intercept ( b ) = -0.02919

Coefficient ( r ) = 0.99997

## CALCULATIONS

$V_{\text{std}} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/760](298/\text{Ta})$

$Q_{\text{std}} = V_{\text{std}}/\text{Time}$

$V_{\text{a}} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/\text{Pa}]$

$Q_{\text{a}} = V_{\text{a}}/\text{Time}$

For subsequent flow rate calculations:

$Q_{\text{std}} = 1/m\{[\text{SQRT}(\text{H}_2\text{O}(\text{Pa}/760)(298/\text{Ta}))]-b\}$

$Q_{\text{a}} = 1/m\{[\text{SQRT}(\text{H}_2\text{O}(\text{Ta}/\text{Pa}))]-b\}$


PREPARED AND CHECKED BY:  
For and On Behalf of **WELLAB Ltd.**

*Patrick Tse*

**PATRICK TSE**  
Laboratory Manager



## TEST REPORT

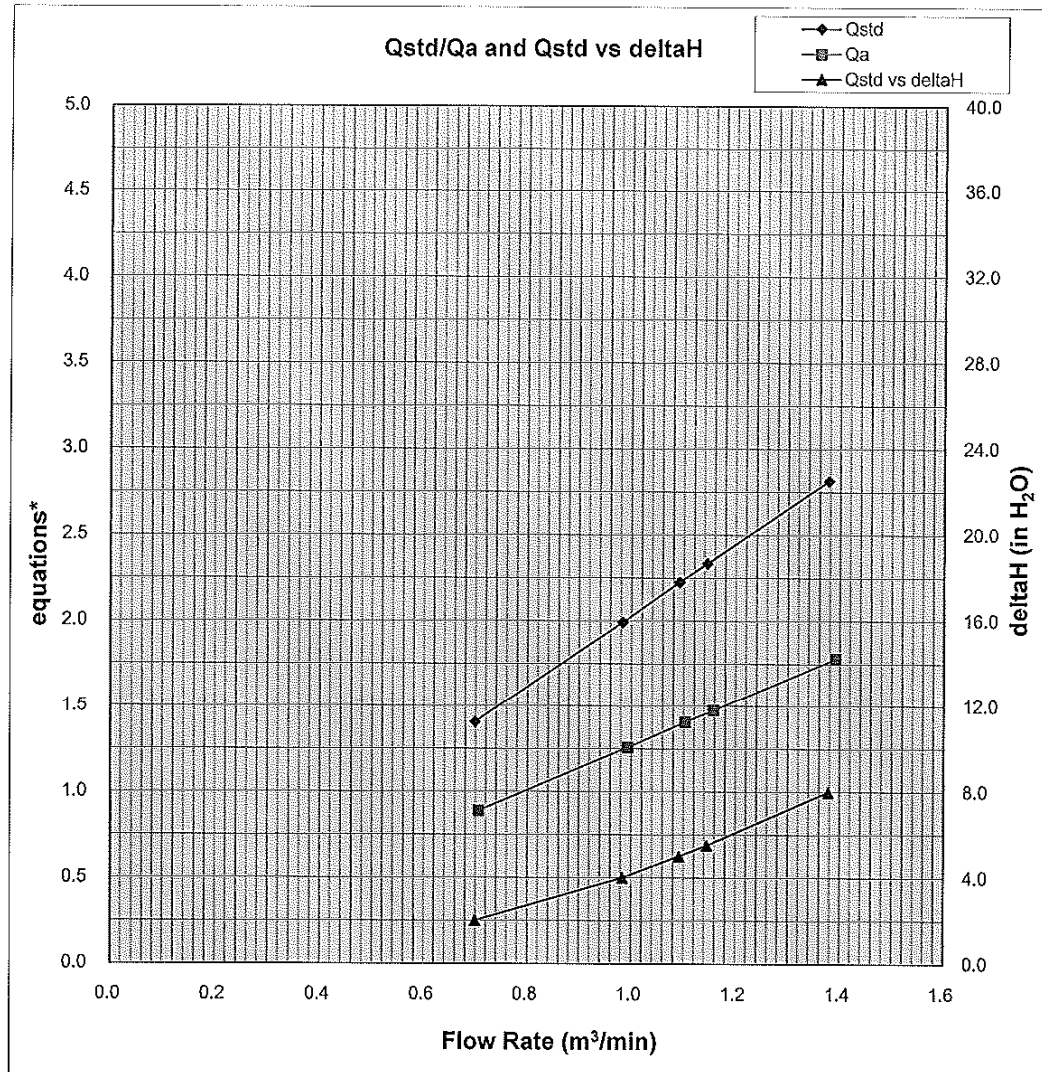

Y-axis equations:

Qstd series:  $\text{SQRT}[\Delta H(\text{Pa}/\text{Pstd})(\text{Tstd}/\text{Ta})]$

Qa series:  $\text{SQRT}[\Delta H(\text{Ta}/\text{Pa})]$

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	CA/140426
Date of Issue:	2014-04-27
Date Received:	2014-04-26
Date Tested:	2014-04-26
Date Completed:	2014-04-27
Next Due Date:	2015-04-26

**ATTN:** Mr. W.K Tang

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: RS232 Integral Vane Digital Anemometer
Manufacturer	: AZ Instrument
Model No.	: AZ8904
Serial No.	: 974835
Equipment No.	: A-03-03

**Test conditions:**

Room Temperature	: 19 degree Celsius
Relative Humidity	: 60%
Pressure	: 101.4 kPa

**Methodology:**

The anemometer has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

	Reference Set Point	Instrument Readings
Measuring Air Velocity, m/s	2.00	2.00
Temperature, °C	21.0	21.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/140104
Date of Issue:	2014-01-05
Date Received:	2014-01-04
Date Tested:	2014-01-04
Date Completed:	2014-01-05
Next Due Date:	2015-01-04

**ATTN:** Mr. W. K. Tang

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 14303
Microphone No.	: 35222
Equipment No.	: N-08-05

**Test conditions:**

Room Temperature	: 19 degree Celsius
Relative Humidity	: 52%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

Remark: 1) This report supersedes the one dated 2012/01/21 with certificate number C/N/120120/1.

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/140822/1
Date of Issue:	2014-08-25
Date Received:	2014-08-22
Date Tested:	2014-08-22
Date Completed:	2014-08-25
Next Due Date:	2015-08-24

**ATTN:** Mr. W.K. Tang

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 21460
Microphone No.	: 43679
Equipment No.	: N-08-09

**Test conditions:**

Room Temperature	: 22 degree Celsius
Relative Humidity	: 55%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/131129/1
Date of Issue:	2013-11-30
Date Received:	2013-11-29
Date Tested:	2013-11-29
Date Completed:	2013-11-30
Next Due Date:	2014-11-29

**ATTN:** Mr. W.K. Tang

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 23853
Microphone No.	: 48530
Equipment No.	: N-08-10

**Test conditions:**

Room Temperature	: 19 degree Celsius
Relative Humidity	: 57%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/130919/3
Date of Issue:	2013-09-21
Date Received:	2013-09-19
Date Tested:	2013-09-21
Date Completed:	2013-09-21
Next Due Date:	2014-09-20

**ATTN:** Mr. W.K. Tang

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10929
Equipment No.	: N-09-01

### Test conditions:

Room Temperature	: 22 degree Celsius
Relative Humidity	: 57%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/140919/4
Date of Issue:	2014-09-21
Date Received:	2014-09-19
Date Tested:	2014-09-21
Date Completed:	2014-09-21
Next Due Date:	2015-09-20

**ATTN:** Mr. W.K. Tang

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10929
Equipment No.	: N-09-01

### Test conditions:

Room Temperature	: 23 degree Celsius
Relative Humidity	: 55%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/131004/1
Date of Issue:	2013-10-05
Date Received:	2013-10-04
Date Tested:	2013-10-04
Date Completed:	2013-10-05
Next Due Date:	2014-10-04

**ATTN:** Mr. W.K. Tang

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 24803
Equipment No.	: N-09-03

### Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 57%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 $\pm$ 0.1 dB
At 114 dB SPL	114.0	114.0 $\pm$ 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager



---

---

**APPENDIX C  
ENVIRONMENTAL MONITORING  
SCHEDULE**

---

---

**Contract No. DE/2009/09 - Construction of Tai Po Sewage Treatment Works - Stage 5 Phase 2B**  
**Impact Air Quality and Noise Monitoring Schedule for September 2014**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep
	1 hr TSP Noise	24 hr TSP	1 hr TSP		1 hr TSP	
7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep
	24 hr TSP		1 hr TSP	1 hr TSP	1 hr TSP Noise	24 hr TSP
14-Sep	15-Sep	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep
	1 hr TSP Noise			1 hr TSP	1 hr TSP 24 hr TSP	
21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	26-Sep	27-Sep
	1 hr TSP Noise	1 hr TSP		1 hr TSP 24 hr TSP		
28-Sep	29-Sep	30-Sep				
	1 hr TSP Noise	1 hr TSP 24 hr TSP				

**Contract No. DE/2009/09 - Construction of Tai Po Sewage Treatment Works - Stage 5 Phase 2B**  
**Tentative Impact Air Quality and Noise Monitoring Schedule for October 2014**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			<b>1-Oct</b>	<b>2-Oct</b>	3-Oct	4-Oct
					1 hr TSP Noise	
<b>5-Oct</b>	6-Oct	7-Oct	8-Oct	9-Oct	10-Oct	11-Oct
	24 hr TSP	1 hr TSP	1 hr TSP	1 hr TSP Noise		24 hr TSP
<b>12-Oct</b>	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct
	1 hr TSP	1 hr TSP Noise			1 hr TSP 24 hr TSP	
<b>19-Oct</b>	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
	1 hr TSP		1 hr TSP Noise	24 hr TSP	1 hr TSP	
<b>26-Oct</b>	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	
		1 hr TSP	1 hr TSP 24 hr TSP	1 hr TSP Noise		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

---

**APPENDIX D**  
**1-HOUR TSP MONITORING RESULTS**  
**AND GRAPHICAL PRESENTATION**

---

## Appendix D - 1-hour TSP Monitoring Results

### Station CAM1

### Government Staff Quarters

Date	Sampling Time	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
					Initial	Final		Initial	Final		Initial	Final			
1-Sep-14	09:00	Sunny	302.9	759.9	3.2811	3.2869	0.0058	23471.1	23472.1	1.0	1.21	1.21	1.21	72.7	80
3-Sep-14	11:00	Sunny	303.7	758.3	3.1918	3.2074	0.0156	23496.1	23497.1	1.0	1.21	1.21	1.21	72.6	215
5-Sep-14	09:00	Cloudy	298.6	758.6	3.2163	3.2250	0.0087	23497.1	23498.1	1.0	1.22	1.22	1.22	73.1	119
10-Sep-14	10:30	Sunny	304.0	758.2	3.1728	3.1770	0.0042	23522.1	23523.1	1.0	1.21	1.21	1.21	72.6	58
11-Sep-14	10:00	Sunny	302.5	758.8	3.2433	3.2506	0.0073	23523.1	23524.1	1.0	1.21	1.21	1.21	72.7	100
12-Sep-14	09:00	Cloudy	301.0	757.5	3.2379	3.2474	0.0095	23524.1	23525.1	1.0	1.21	1.21	1.21	72.8	130
15-Sep-14	11:00	Cloudy	304.2	754.3	3.1572	3.1643	0.0071	23549.1	23550.1	1.0	1.21	1.21	1.21	72.4	98
18-Sep-14	09:00	Sunny	303.1	762.2	3.1959	3.2109	0.0150	23550.1	23551.1	1.0	1.21	1.21	1.21	72.8	206
19-Sep-14	09:00	Cloudy	303.1	758.4	3.1963	3.2076	0.0113	23551.1	23552.1	1.0	1.21	1.21	1.21	72.7	156
22-Sep-14	09:00	Sunny	300.6	757.5	3.1806	3.1901	0.0095	23576.1	23577.1	1.0	1.22	1.21	1.21	72.9	130
23-Sep-14	09:00	Sunny	301.9	759.2	3.2129	3.2177	0.0048	23577.1	23578.1	1.0	1.21	1.21	1.21	72.8	66
25-Sep-14	09:00	Sunny	301.1	761.9	3.2583	3.2630	0.0047	23578.1	23579.1	1.0	1.22	1.22	1.22	73.0	64
29-Sep-14	09:00	Sunny	302.1	761.7	3.1735	3.1807	0.0072	23603.1	23604.1	1.0	1.22	1.21	1.22	72.9	99
30-Sep-14	09:00	Sunny	302.7	761.6	3.1790	3.1836	0.0046	23604.1	23605.1	1.0	1.21	1.21	1.21	72.8	63
														Min	58
														Max	215
														Average	113

### Station CAM2

### Heng Hing Printing Centre

Date	Sampling Time	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
					Initial	Final		Initial	Final		Initial	Final			
1-Sep-14	09:00	Sunny	302.9	759.9	3.2343	3.2399	0.0056	29746.3	29747.3	1.0	1.22	1.22	1.22	73.3	76
3-Sep-14	11:00	Sunny	303.7	758.3	3.2424	3.2590	0.0166	29771.3	29772.3	1.0	1.22	1.22	1.22	73.1	227
5-Sep-14	09:00	Cloudy	298.6	758.6	3.2286	3.2368	0.0082	29772.3	29773.3	1.0	1.23	1.23	1.23	73.7	111
10-Sep-14	10:45	Sunny	304.0	758.2	3.1472	3.1536	0.0064	29797.3	29798.3	1.0	1.22	1.22	1.22	73.1	88
11-Sep-14	10:00	Sunny	302.5	758.8	3.2192	3.2283	0.0091	29798.3	29799.3	1.0	1.22	1.22	1.22	73.3	124
12-Sep-14	15:30	Cloudy	301.0	757.5	3.2398	3.2484	0.0086	29799.3	29800.3	1.0	1.22	1.22	1.22	73.4	117
15-Sep-14	10:30	Cloudy	304.2	754.5	3.2549	3.2633	0.0084	29824.3	29825.3	1.0	1.21	1.21	1.21	72.9	115
18-Sep-14	09:00	Sunny	303.1	762.2	3.2829	3.2973	0.0144	29825.3	29826.3	1.0	1.22	1.22	1.22	73.3	196
19-Sep-14	09:00	Cloudy	303.1	758.4	3.2486	3.2629	0.0143	29826.3	29827.3	1.0	1.22	1.22	1.22	73.2	195
22-Sep-14	09:00	Sunny	300.6	757.5	3.1936	3.2009	0.0073	29851.3	29852.3	1.0	1.22	1.22	1.22	73.4	99
23-Sep-14	09:00	Sunny	301.9	759.2	3.2418	3.2514	0.0096	29852.3	29853.3	1.0	1.22	1.22	1.22	73.3	131
25-Sep-14	09:00	Sunny	301.1	761.9	3.2454	3.2555	0.0101	29853.3	29854.3	1.0	1.23	1.23	1.23	73.6	137
29-Sep-14	09:00	Sunny	302.1	761.7	3.1868	3.1960	0.0092	29878.3	29879.3	1.0	1.22	1.22	1.22	73.4	125
30-Sep-14	09:00	Sunny	302.7	761.6	3.2032	3.2116	0.0084	29879.3	29880.3	1.0	1.22	1.22	1.22	73.4	115
														Min	76
														Max	227
														Average	133




## Appendix D - 1-hour TSP Monitoring Results

Station CAM3

Talcon Industrial Ltd

Date	Sampling Time	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
					Initial	Final		Initial	Final		Initial	Final			
1-Sep-14	09:00	Sunny	302.9	759.9	3.2241	3.2312	0.0071	23880.9	23881.9	1.0	1.22	1.22	1.22	73.0	97
3-Sep-14	11:00	Sunny	303.7	758.3	3.2560	3.2734	0.0174	23905.9	23906.9	1.0	1.21	1.21	1.21	72.8	239
5-Sep-14	09:00	Cloudy	298.6	758.6	3.2245	3.2328	0.0083	23906.9	23907.9	1.0	1.22	1.22	1.22	73.4	113
10-Sep-14	10:45	Sunny	304.0	758.2	3.1948	3.2015	0.0067	23931.9	23932.9	1.0	1.21	1.21	1.21	72.8	92
11-Sep-14	10:00	Sunny	302.5	758.8	3.2231	3.2346	0.0115	23932.9	23933.9	1.0	1.22	1.22	1.22	73.0	158
12-Sep-14	15:30	Cloudy	301.0	757.5	3.2359	3.2434	0.0075	23933.9	23934.9	1.0	1.22	1.22	1.22	73.1	103
15-Sep-14	10:30	Cloudy	304.2	754.5	3.2593	3.2708	0.0115	23958.9	23959.9	1.0	1.21	1.21	1.21	72.6	158
18-Sep-14	09:00	Sunny	303.1	762.2	3.2692	3.2858	0.0166	23959.9	23960.9	1.0	1.22	1.22	1.22	73.1	227
19-Sep-14	09:00	Cloudy	303.1	758.4	3.2464	3.2601	0.0137	23960.9	23961.9	1.0	1.21	1.21	1.21	72.9	188
22-Sep-14	09:00	Sunny	300.6	757.5	3.1489	3.1595	0.0106	23985.9	23986.9	1.0	1.22	1.22	1.22	73.1	145
23-Sep-14	09:00	Sunny	301.9	759.2	3.2267	3.2392	0.0125	23986.9	23987.9	1.0	1.22	1.22	1.22	73.1	171
25-Sep-14	09:00	Sunny	301.1	761.9	3.2121	3.2216	0.0095	23987.9	23988.9	1.0	1.22	1.22	1.22	73.3	130
29-Sep-14	09:00	Sunny	302.1	761.7	3.1861	3.1945	0.0084	24012.9	24013.9	1.0	1.22	1.22	1.22	73.1	115
30-Sep-14	09:00	Sunny	302.7	761.6	3.2296	3.2388	0.0092	24013.9	24014.9	1.0	1.22	1.22	1.22	73.1	126
														Min	92
														Max	239
														Average	147

## 1-hr TSP Concentration Levels

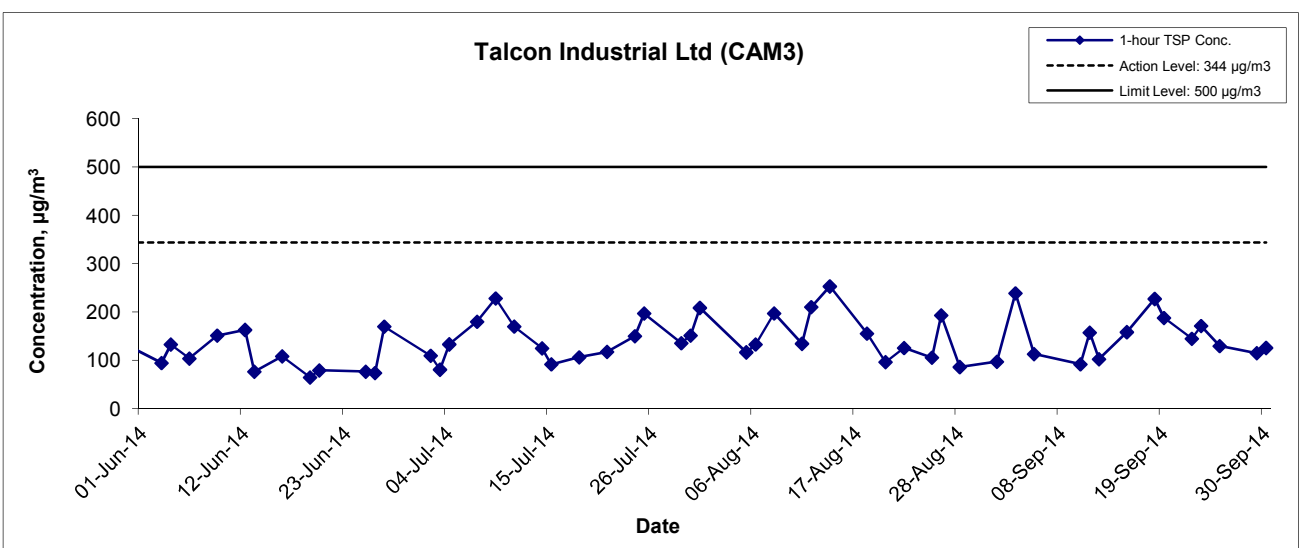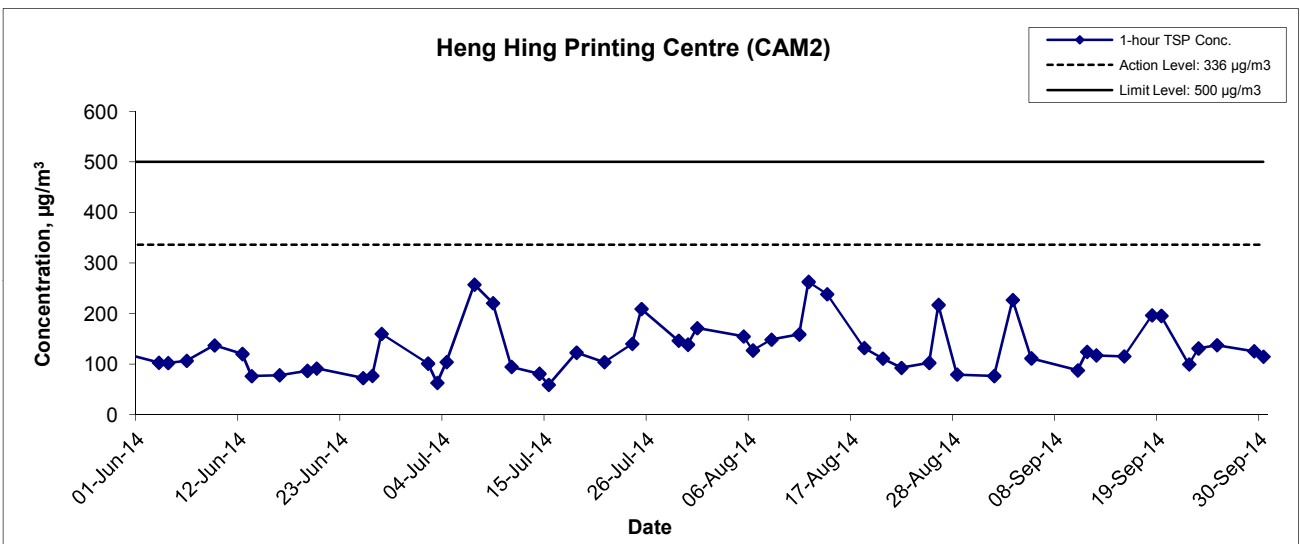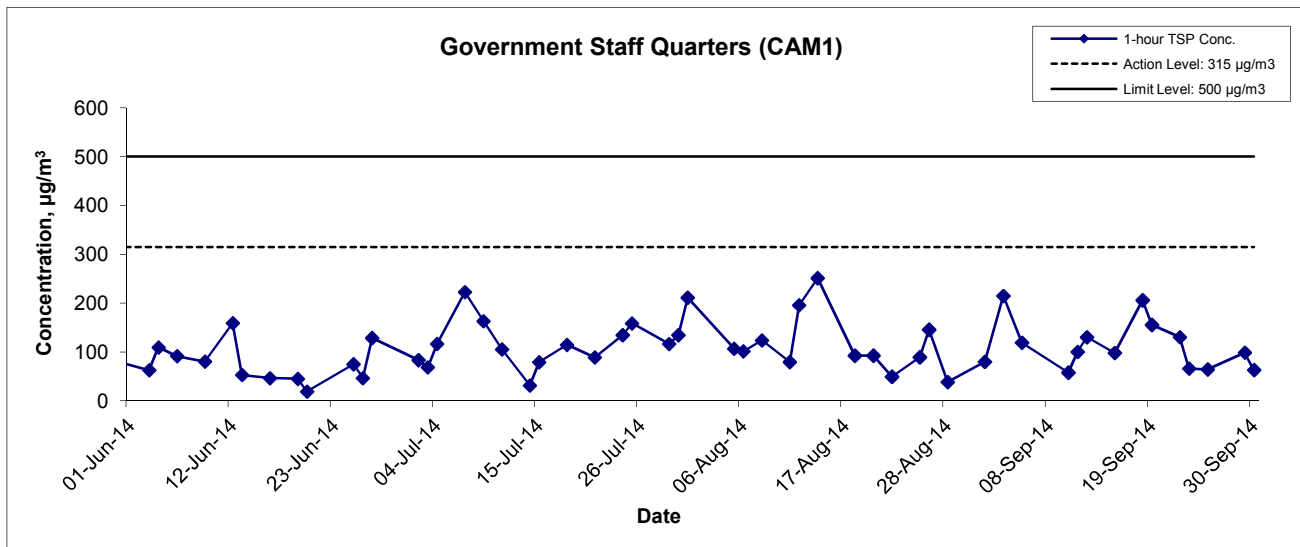

Title	Contract No. DC/2009/09	Scale	Project No.	CINOTECH
	Construction of Tai Po Sewage Treatment Works - Stage V Phase II B	N.T.S	MA0010	
	Graphical Presentation of 1-hour TSP Impact Monitoring Results	Date Sep 14	Appendix D	

---

**APPENDIX E**  
**24-HOUR TSP MONITORING RESULTS**  
**AND GRAPHICAL PRESENTATION**

---



## Appendix E - 24-hour TSP Monitoring Results

### Station CAM1

#### Government Staff Quarters

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
2-Sep-14	Sunny	303.2	761.3	3.2577	3.3387	0.0810	23472.1	23496.1	24.0	1.21	1.21	1.21	1746.4	46
8-Sep-14	Cloudy	301.9	757.7	3.3087	3.3785	0.0698	23498.1	23522.1	24.0	1.21	1.21	1.21	1746.0	40
13-Sep-14	Cloudy	302.7	756.6	3.1767	3.2229	0.0462	23525.1	23549.1	24.0	1.21	1.21	1.21	1742.8	27
19-Sep-14	Cloudy	306.2	757.7	3.1408	3.3571	0.2163	23552.1	23576.1	24.0	1.21	1.20	1.20	1735.1	125
25-Sep-14	Sunny	303.2	760.3	3.1693	3.2224	0.0531	23579.1	23603.1	24.0	1.21	1.21	1.21	1745.4	30
30-Sep-14	Sunny	306.3	758.7	3.2699	3.4548	0.1849	23605.1	23629.1	24.0	1.21	1.21	1.21	1736.0	107
													Min	27
													Max	125
													Average	62

### Station CAM2

#### Heng Hing Printing Centre




Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
2-Sep-14	Sunny	303.2	761.3	3.2529	3.3450	0.0921	29747.3	29771.3	24.0	1.22	1.22	1.22	1759.0	52
8-Sep-14	Cloudy	301.9	757.7	3.1772	3.2700	0.0928	29773.3	29797.3	24.0	1.22	1.22	1.22	1758.6	53
13-Sep-14	Cloudy	302.7	756.6	3.2970	3.3498	0.0528	29800.3	29824.3	24.0	1.22	1.22	1.22	1755.3	30
19-Sep-14	Cloudy	306.2	757.7	3.1916	3.4200	0.2284	29827.3	29851.3	24.0	1.21	1.21	1.21	1747.2	131
25-Sep-14	Sunny	303.2	760.3	3.1518	3.2348	0.0830	29854.3	29878.3	24.0	1.22	1.22	1.22	1757.9	47
30-Sep-14	Sunny	306.3	758.7	3.2206	3.4244	0.2038	29880.3	29904.3	24.0	1.21	1.21	1.21	1748.1	117
													Min	30
													Max	131
													Average	72

### Station CAM3

#### Talcon Industrial Ltd

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
2-Sep-14	Sunny	303.2	761.3	3.2659	3.3939	0.1280	23881.9	23905.9	24.0	1.22	1.22	1.22	1752.0	73
8-Sep-14	Cloudy	301.9	757.7	3.1828	3.2747	0.0919	23907.9	23931.9	24.0	1.22	1.22	1.22	1751.6	52
13-Sep-14	Cloudy	302.7	756.6	3.2961	3.3572	0.0611	23934.9	23958.9	24.0	1.21	1.21	1.21	1748.1	35
19-Sep-14	Cloudy	306.2	757.7	3.2263	3.4718	0.2455	23961.9	23985.9	24.0	1.21	1.21	1.21	1739.7	141
25-Sep-14	Sunny	303.2	760.3	3.1470	3.2343	0.0873	23988.9	24012.9	24.0	1.22	1.22	1.22	1750.9	50
30-Sep-14	Sunny	306.3	758.7	3.1660	3.4074	0.2414	24014.9	24038.9	24.0	1.21	1.21	1.21	1740.7	139
													Min	35
													Max	141
													Average	82

## 24-hr TSP Concentration Levels

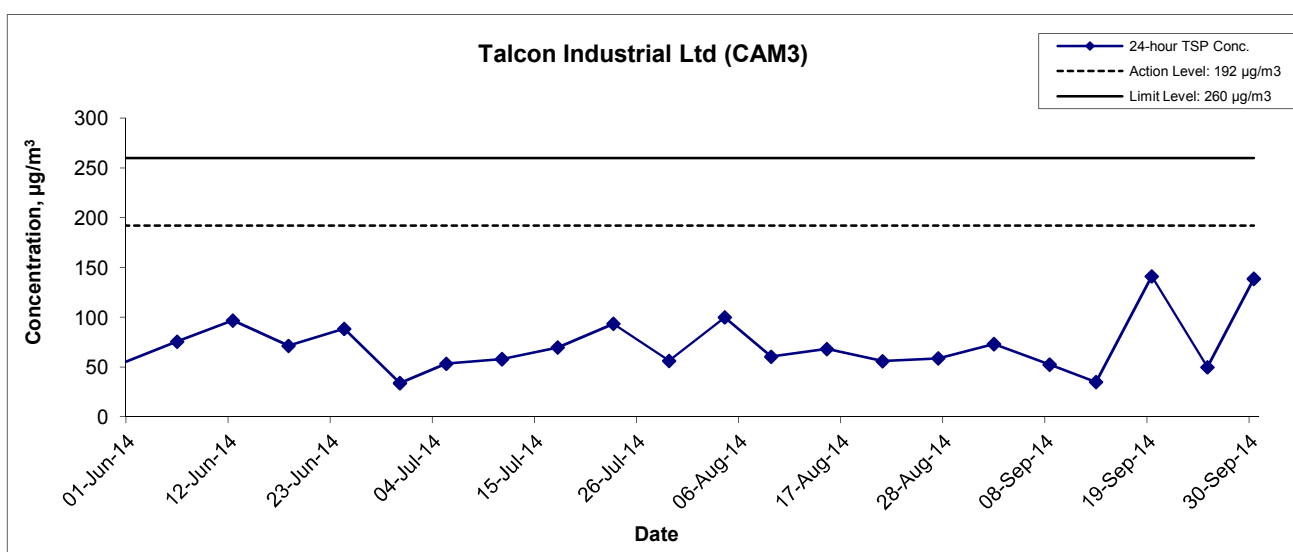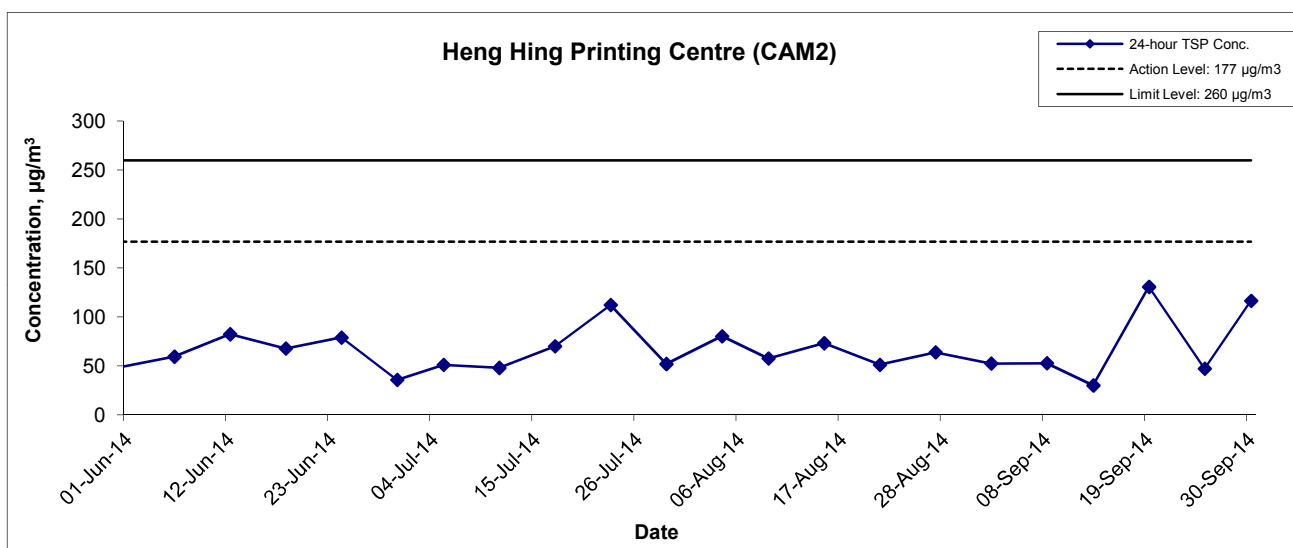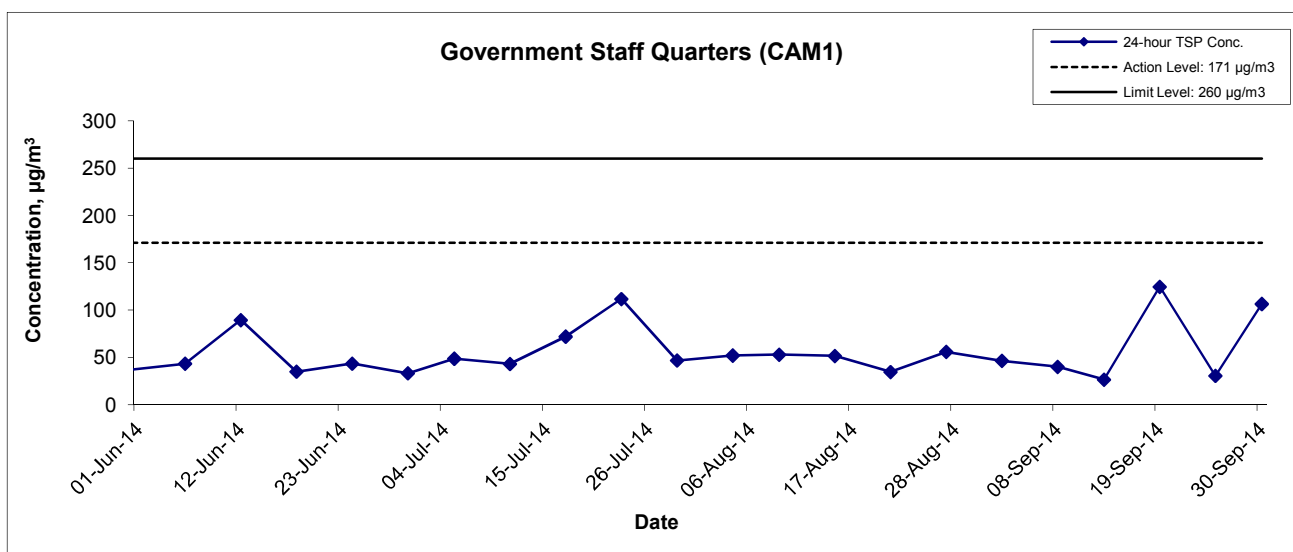

Title	Contract No. DC/2009/09	Scale	Project	CINOTECH
	Construction of Tai Po Sewage Treatment Works - Stage V Phase II B	N.T.S	No. MA0010	
	Graphical Presentation of 24-hour TSP Impact Monitoring Results	Date	Appendix	
		Sep 14	E	

---

---

**APPENDIX F**  
**NOISE MONITORING RESULTS AND**  
**GRAPHICAL PRESENTATION**


---

---

## Appendix F - Noise Monitoring Results

Location NM1 - Government Staff Quarters					
Date	Time	Weather	dB (A) (30-min)		
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>
1-Sep-14	11:10	Sunny	58.4	59.2	57.2
12-Sep-14	16:50	Cloudy	68.2	72.6	65.4
15-Sep-14	11:20	Cloudy	60.9	61.9	60.0
22-Sep-14	09:05	Cloudy	63.5	65.3	59.1
29-Sep-14	13:00	Sunny	62.4	65.8	58.9
Average			64.0	65.0	60.1
Minimum			58.4	59.2	57.2
Maximum			68.2	72.6	65.4

## Noise Levels

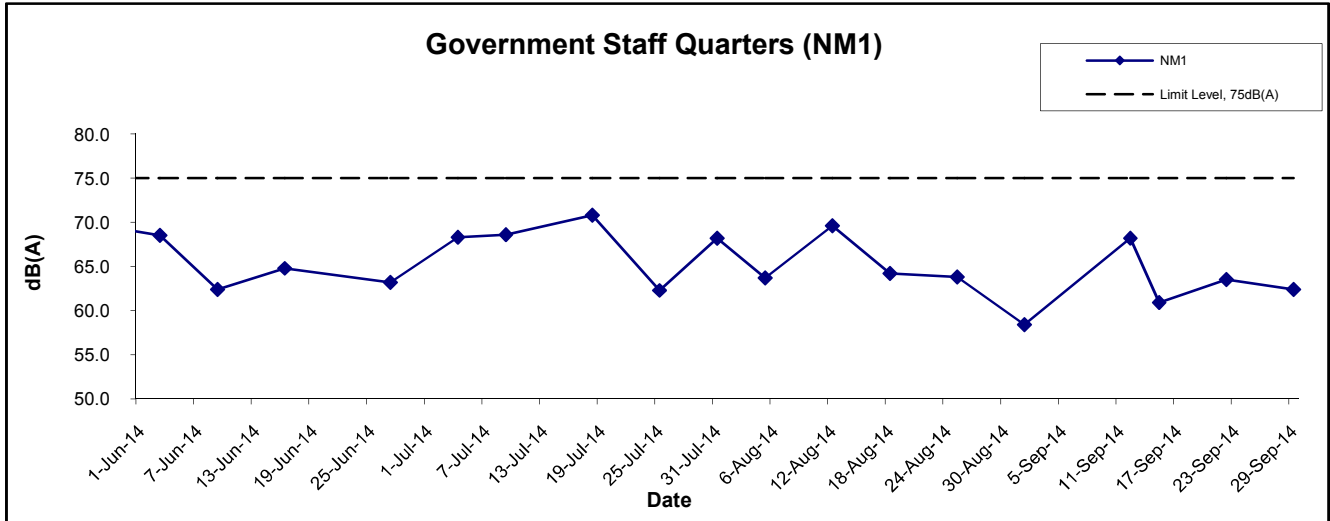

<b>Title</b> Contract No. DC/2009/09 Construction of Tai Po Sewage Treatment Works - Stage V Phase II B Graphical Presentation of Construction Noise Monitoring Results	<b>Scale</b> N.T.S	<b>Project No.</b> MA0010	
	<b>Date</b> Sep 14	<b>Appendix</b> F	

---

**APPENDIX G**  
**SUMMARY OF EXCEEDANCE**

---

## **APPENIDX G – SUMMARY OF EXCEEDANCE**

**Reporting Month:** September 2014

*a) Exceedance Report for 1-hr TSP (NIL)*

*b) Exceedance Report for 24-hr TSP (NIL)*

*c) Exceedance Report for Construction Noise (NIL)*

---

**APPENDIX H**  
**SITE AUDIT SUMMARY**

---



**Supply and Installation of Electrical and Mechanical Equipment for  
Tai Po Sewage Treatment Works Stage 5 Phase 2B**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	140904
Date	4 September 2014 (Thursday)
Time	9:45 – 10:45

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
140904-R01 140904-R02	<p><b>Part C - Water Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part E – Noise</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste / Chemical Management</b></p> <ul style="list-style-type: none"> <li>Plastic bottles should be sorted for recycling.</li> <li>Oil leaking from the control device at aeration tank should be cleared.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H – Remark</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Others</b></p> <ul style="list-style-type: none"> <li>Follow-up on the previous audit session (Ref. No.140825), no environmental deficiency was identified during the site inspection.</li> </ul>	F1 F7i

	Name	Signature	Date
Recorded by	Harris Wong		4 September 2014
Checked by	Dr. Priscilla Choy		4 September 2014

Contract No. DE/2009/09

**Supply and Installation of Electrical and Mechanical Equipment for  
Tai Po Sewage Treatment Works Stage 5 Phase 2B**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	140912
Date	12 September 2014 (Friday)
Time	9:45 – 10:15

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
140912-R01	<p><b>Part C - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E – Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• Cardboards should be sorted for recycling.</li></ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part H – Remark</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• Follow-up on the previous audit session (Ref. No.140904), all environmental deficiencies were observed improved/rectified by Contractor during site inspection.</li></ul>	Fliii

	Name	Signature	Date
Recorded by	Harris Wong		12 September 2014
Checked by	Dr. Priscilla Choy		12 September 2014

Contract No. DE/2009/09

**Supply and Installation of Electrical and Mechanical Equipment for  
Tai Po Sewage Treatment Works Stage 5 Phase 2B**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	140917
Date	17 September 2014 (Friday)
Time	10:00 – 10:45

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part C - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E - Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• Follow-up on the previous audit session (Ref. No.140912), all environmental deficiencies were observed improved/rectified by Contractor during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Harris Wong		17 September 2014
Checked by	Dr. Priscilla Choy		17 September 2014

**Supply and Installation of Electrical and Mechanical Equipment for  
Tai Po Sewage Treatment Works Stage 5 Phase 2B**



## Record Summary of Environmental Site Inspection

## Inspection Information

Checklist Reference Number	140923
Date	23 September 2014 (Tuesday)
Time	10:00 – 11:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part C - Water Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part E - Noise</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste / Chemical Management</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Others</b></p> <ul style="list-style-type: none"> <li>Follow-up on the previous audit session (Ref. No.140917), all environmental deficiencies were observed improved/rectified by Contractor during site inspection.</li> </ul>	

	Name	Signature	Date
Recorded by	Harris Wong		23 September 2014
Checked by	Dr. Priscilla Choy		23 September 2014



**Supply and Installation of Electrical and Mechanical Equipment for  
Tai Po Sewage Treatment Works Stage 5 Phase 2B**

**Record Summary of Environmental Site Inspection****Inspection Information**

Checklist Reference Number	140929
Date	29 September 2014 (Monday)
Time	10:00 – 11:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part C - Water Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part E – Noise</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste / Chemical Management</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H – Remark</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Others</b></p> <ul style="list-style-type: none"> <li>Follow-up on the previous audit session (Ref. No.140923), all environmental deficiencies were observed improved/rectified by Contractor during site inspection.</li> </ul>	

	Name	Signature	Date
Recorded by	Harris Wong		29 September 2014
Checked by	Dr. Priscilla Choy		29 September 2014

---

**APPENDIX I**  
**EVENT ACTION PLANS**

---

## APPENDIX I (1) – Event Action Plan for Air Quality Monitoring (Construction Phase)

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b>ACTION LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IC(E) and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing; 2. Ensure remedial measures properly implemented.	1. Submit proposals for remedial actions to IEC within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
<b>LIMIT LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Contractor, IEC, ER, and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

## APPENDIX I (2) – Event Action Plan for Construction Noise Monitoring (Construction Phase)

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b><i>ACTION LEVEL</i></b>	<ol style="list-style-type: none"> <li>1. Notify IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analyzed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC;</li> <li>2. Implement noise mitigation proposals.</li> </ol>
<b><i>LIMIT LEVEL</i></b>	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC, ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>



---

**APPENDIX J  
UPDATED ENVIRONMENTAL  
MITIGATION IMPLEMENTATION  
SCHEDULE**

---

**APPENDIX J – Updated Environmental Mitigation Implementation Schedule  
(During Construction Phase)**

Type of Impact	Recommended Mitigation Measures	Status
<b>Air Quality</b>	Dust mitigation measures stipulated in the <i>Air Pollution Control (Construction Dust) Regulation</i> shall be incorporated to control dust emission. Notice shall be given to authority prior to commencing of work	√
<b>Noise</b>	Use of quiet PME	N/A
	<p>Good Site Practice</p> <ul style="list-style-type: none"> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>Mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	√
<b>Water Quality</b>	The practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted to minimize the potential water quality impacts from construction site runoff and various construction activities. The recommendation to install perimeter drains to collect site runoff and to properly treat the runoff by settlement tank/treatment system shall apply to all sites including those for mainlaying works. Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the existing WSD saltwater intake at Tai Po.	√
	A discharge licence needs to be applied from EPD for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies with all the standards listed in the TM. Reuse and recycling of the treated effluent can minimize water consumption and reduce the effluent discharge volume. The beneficial uses of the treated effluent may include dust suppression, wheel washing and general cleaning. Monitoring of the discharge quality of treated effluent should be part of the Environmental Monitoring and Audit (EM&A) programme. Detailed effluent sampling programme for water quality control during construction phase should be submitted to EPD, AFCD and WSD for approval prior to commencement of the construction works.	N/A
	The construction programme should be properly planned to minimize soil excavation, if any, in rainy seasons. This prevents soil erosion from exposed soil surfaces. Any exposed soil surfaces should also be properly protected to minimize dust emission. In areas where a large amount of exposed soils exist, earth bunds or sand bags should be provided. Exposed stockpiles should be covered with tarpaulin or impervious sheets at all time. The stockpiles of materials should be placed in the locations away from any stream courses so as to avoid releasing materials into the water bodies. Final surfaces of earthworks should be compacted and protected by permanent work. It is suggested that haul roads should be paved with concrete and the temporary access roads are protected using crushed stone or gravel, wherever practicable. Wheel washing facilities should be provided at all site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.	√
	Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. It is recommended to clean the construction sites on a regular basis.	√

Type of Impact	Recommended Mitigation Measures	Status
	It is recommended to provide sufficient chemical toilets in the works areas. The toilet facilities should not be less than 30 m from any watercourse. A licensed waste collector should be deployed to clean the chemical toilets on a regular basis. The construction workers can also make use of the existing toilet facilities within the TPSTW as necessary.	√
	Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the project. Implementation of environmental audit on the construction site can provide an effective control of any malpractices and can achieve continual improvement of environmental performance on site.	√
	It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	√
	Any service shop and minor maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken with the areas appropriately equipped to control these discharges.	√
	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport</li> <li>• Chemical waste containers should be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	√
	Marine water quality monitoring should be carried out under emergency condition or during maintenance of the THEES tunnel to verify the findings of the water quality modelling. It is recommended that the maintenance of the THEES tunnel, if unavoidable, should be conducted during winter season or low flow periods and to avoid the “blooming” season of algae (normally from April to June) if practicable. Details of the monitoring requirements are specified in the EM&A Manual.	N/A

Type of Impact	Recommended Mitigation Measures	Status
<b>Waste Management</b>	<p>Good site practices during the construction activities include: □</p> <ul style="list-style-type: none"> <li>Nomination of approved personnel, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.</li> <li>Training of site personnel in proper waste management and chemical waste handling procedures.</li> <li>Provision of sufficient waste disposal points and regular collection for disposal.</li> <li>Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.</li> <li>Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.</li> <li>A Waste Management Plan shall be prepared and this WMP shall be submitted to the Engineer for approval. One may make reference to ETWB TCW No. 15/2003 for details.</li> <li>In order to monitor the disposal of C&amp;D materials at landfills and public filling areas, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. One may make reference to WBTC No. 21/2002 for details.</li> <li>A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) shall be proposed.</li> </ul>	√
	<p>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>To encourage collection of aluminum cans by individual collectors, separate labelled bins shall be provided to segregate this waste from other general refuse generated by the work force.</li> <li>Any unused chemicals or those with remaining functional capacity shall be recycled.</li> <li>Maximize the use of reusable steel formwork to reduce the amount of C&amp;D material.</li> <li>Prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimize the quantity of waste to be disposed of to landfill.</li> <li>Proper storage and site practices to minimize the potential for damage or contamination of construction materials.</li> <li>Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.</li> <li>Minimize over ordering of concrete, mortars and cement grout by doing careful check before ordering</li> </ul>	√
	<p><i>General Refuse</i></p> <p>General refuse shall be stored in enclosed bins or compaction units separate from C&amp;D material. A reputable waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&amp;D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material.</p>	√
	<p><i>Construction &amp; Demolition (C&amp;D) Material</i></p> <p>C&amp;D material generated from the site formation and demolition works shall be sorted on-site into inert C&amp;D material (i.e. public fill) and C&amp;D waste. In order to minimise the impact resulting from collection and transportation of C&amp;D material for off-site disposal, the excavated material comprising fill material shall be reused on-site as backfilling material as far as practicable. C&amp;D waste, such as wood, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated within the site for temporary stockpiling of C&amp;D material and to facilitate the sorting process.</p>	√

Type of Impact	Recommended Mitigation Measures	Status
	<i>Bentonite Slurry</i> Bentonite slurries used in construction works should be reconditioned and reused wherever practicable. Residual used bentonite slurry should be disposed of from the site as soon as possible. The Contractor should explore alternative disposal outlets for the residual used bentonite slurry and disposal at landfill should be the last resort.	N/A

**Note:**

- √ – Compliance of mitigation measures  
X – Non-compliance of mitigation measures  
N/A – Not applicable

---

---

**APPENDIX K  
WASTE GENERATION IN THE  
REPORTING MONTH**

---

---

Name of Department: Drainage Services Department

Contract No. : DE/2009/09

### Monthly Summary - Waste Flow Table for 2014

Month	Annual Quantities of Inert C&D Materials Generated Monthly						Annual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in tonne)
Jan	0	0	0	0	0	0	0	0.13	0.05	0	1.6
Feb	0	0	0	0	0	0	0	0.14	0.05	0	0
Mar	0	0	0	0	0	0	0	0	0	0	1.9
Apr	0	0	0	0	0	0	11.1	0.13	0.03	0	4.6
May	3.6	3.6	0	0	3.6	0	0	0.15	0	0	2.4
June	0	0	0	0	0	0	0	0	0	0	4.1
July	4	4	0	0	4	0	0	0	0	0	0
Aug	0	0	0	0	0	0	0	0	0	0	0
Sept	0	0	0	0	0	0	0	0.1	0	0	1.7
Oct											
Nov											
Dec											
Total	7.6	7.6	0	0	7.6	0	11.1	0.65	0.13	0	16.3

Forecast of Total Quantities of C&D Materials to be Generated from the Contractor										
Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in m <sup>3</sup> )	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in tonne)
0	20	0	0	20	0	100	100	50	10	500

- Notes:
- (1) The performance targets are given in PS Clause 1.40.8(14).
  - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
  - (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m<sup>3</sup>. (PS Clause 1.40.7(4)(b) refers.

---

---

**APPENDIX L**  
**COMPLAINT LOG**

---

---



**APPENDIX L – COMPLAINT LOG****Reporting Month:** September 2014

<b>Log Ref.</b>	<b>Location</b>	<b>Received Date</b>	<b>Details of Complaint</b>	<b>Investigation/Mitigation Action</b>	<b>Status</b>
N/A	N/A	N/A	N/A	N/A	N/A

**Remarks:** No environmental complaint was received in the reporting month.

---


---

**APPENDIX M**  
**CONSTRUCTION PROGRAMME**


---

---


Section II Works Programme

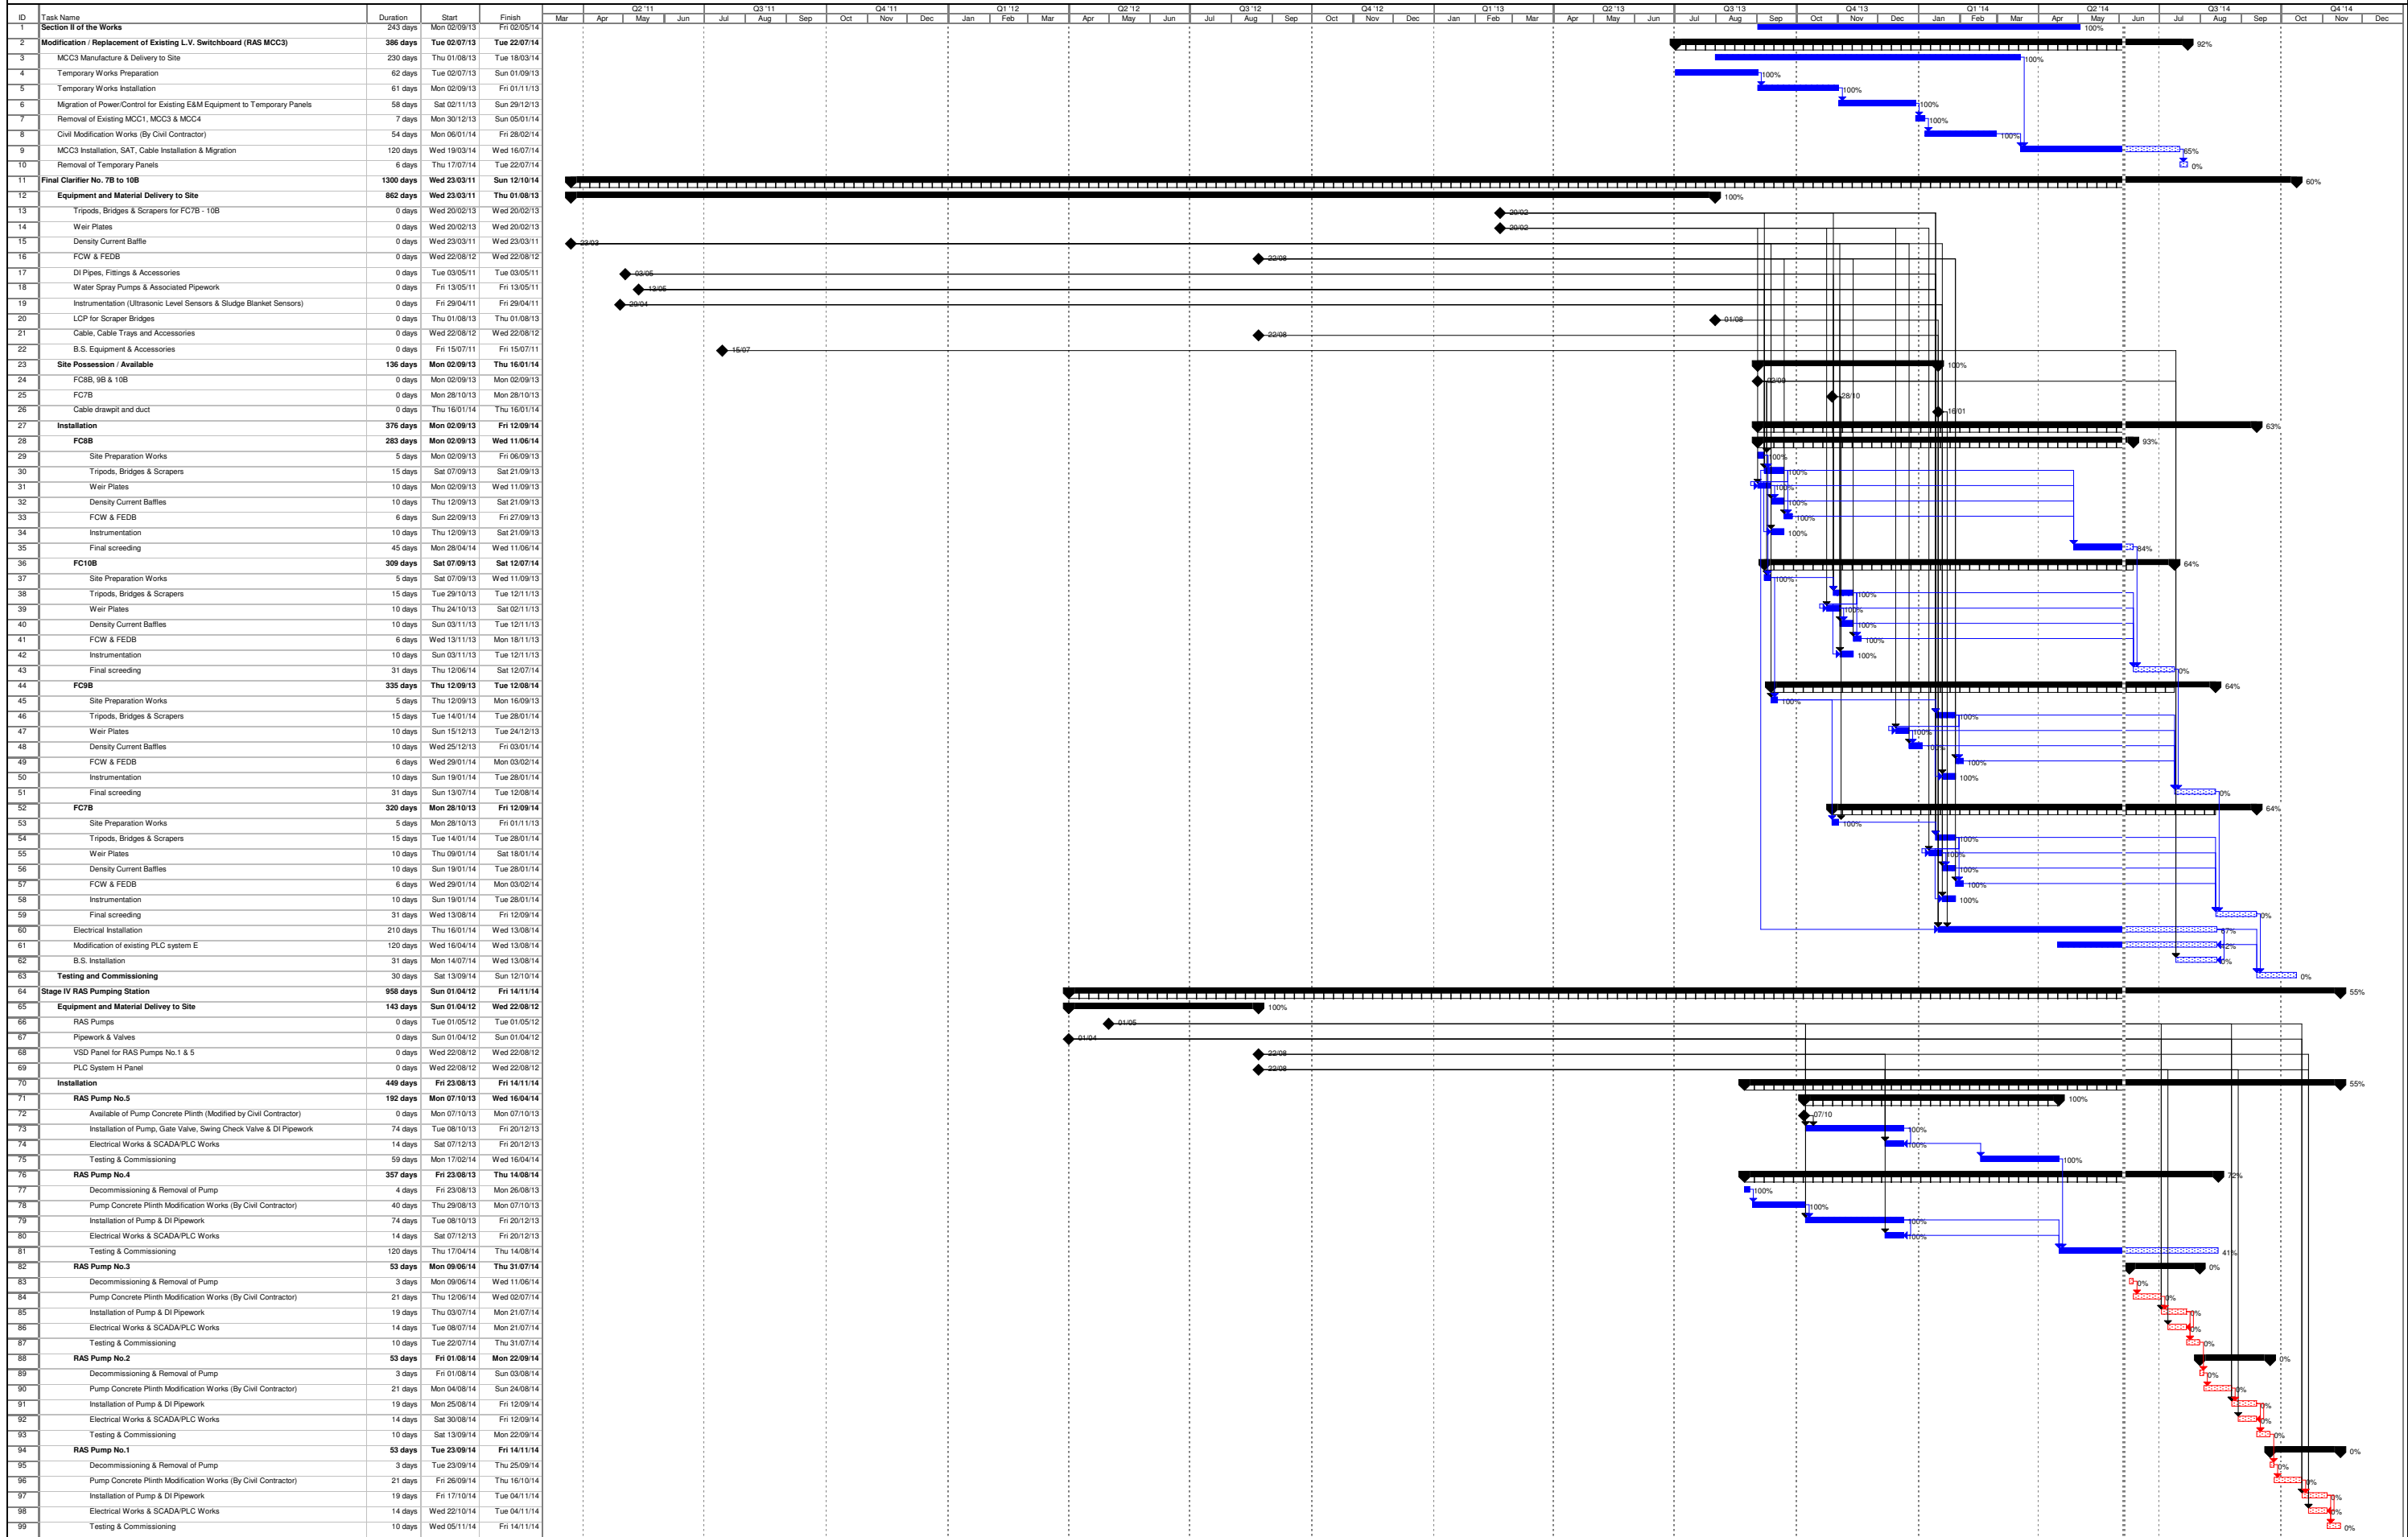


Section III Works Programme

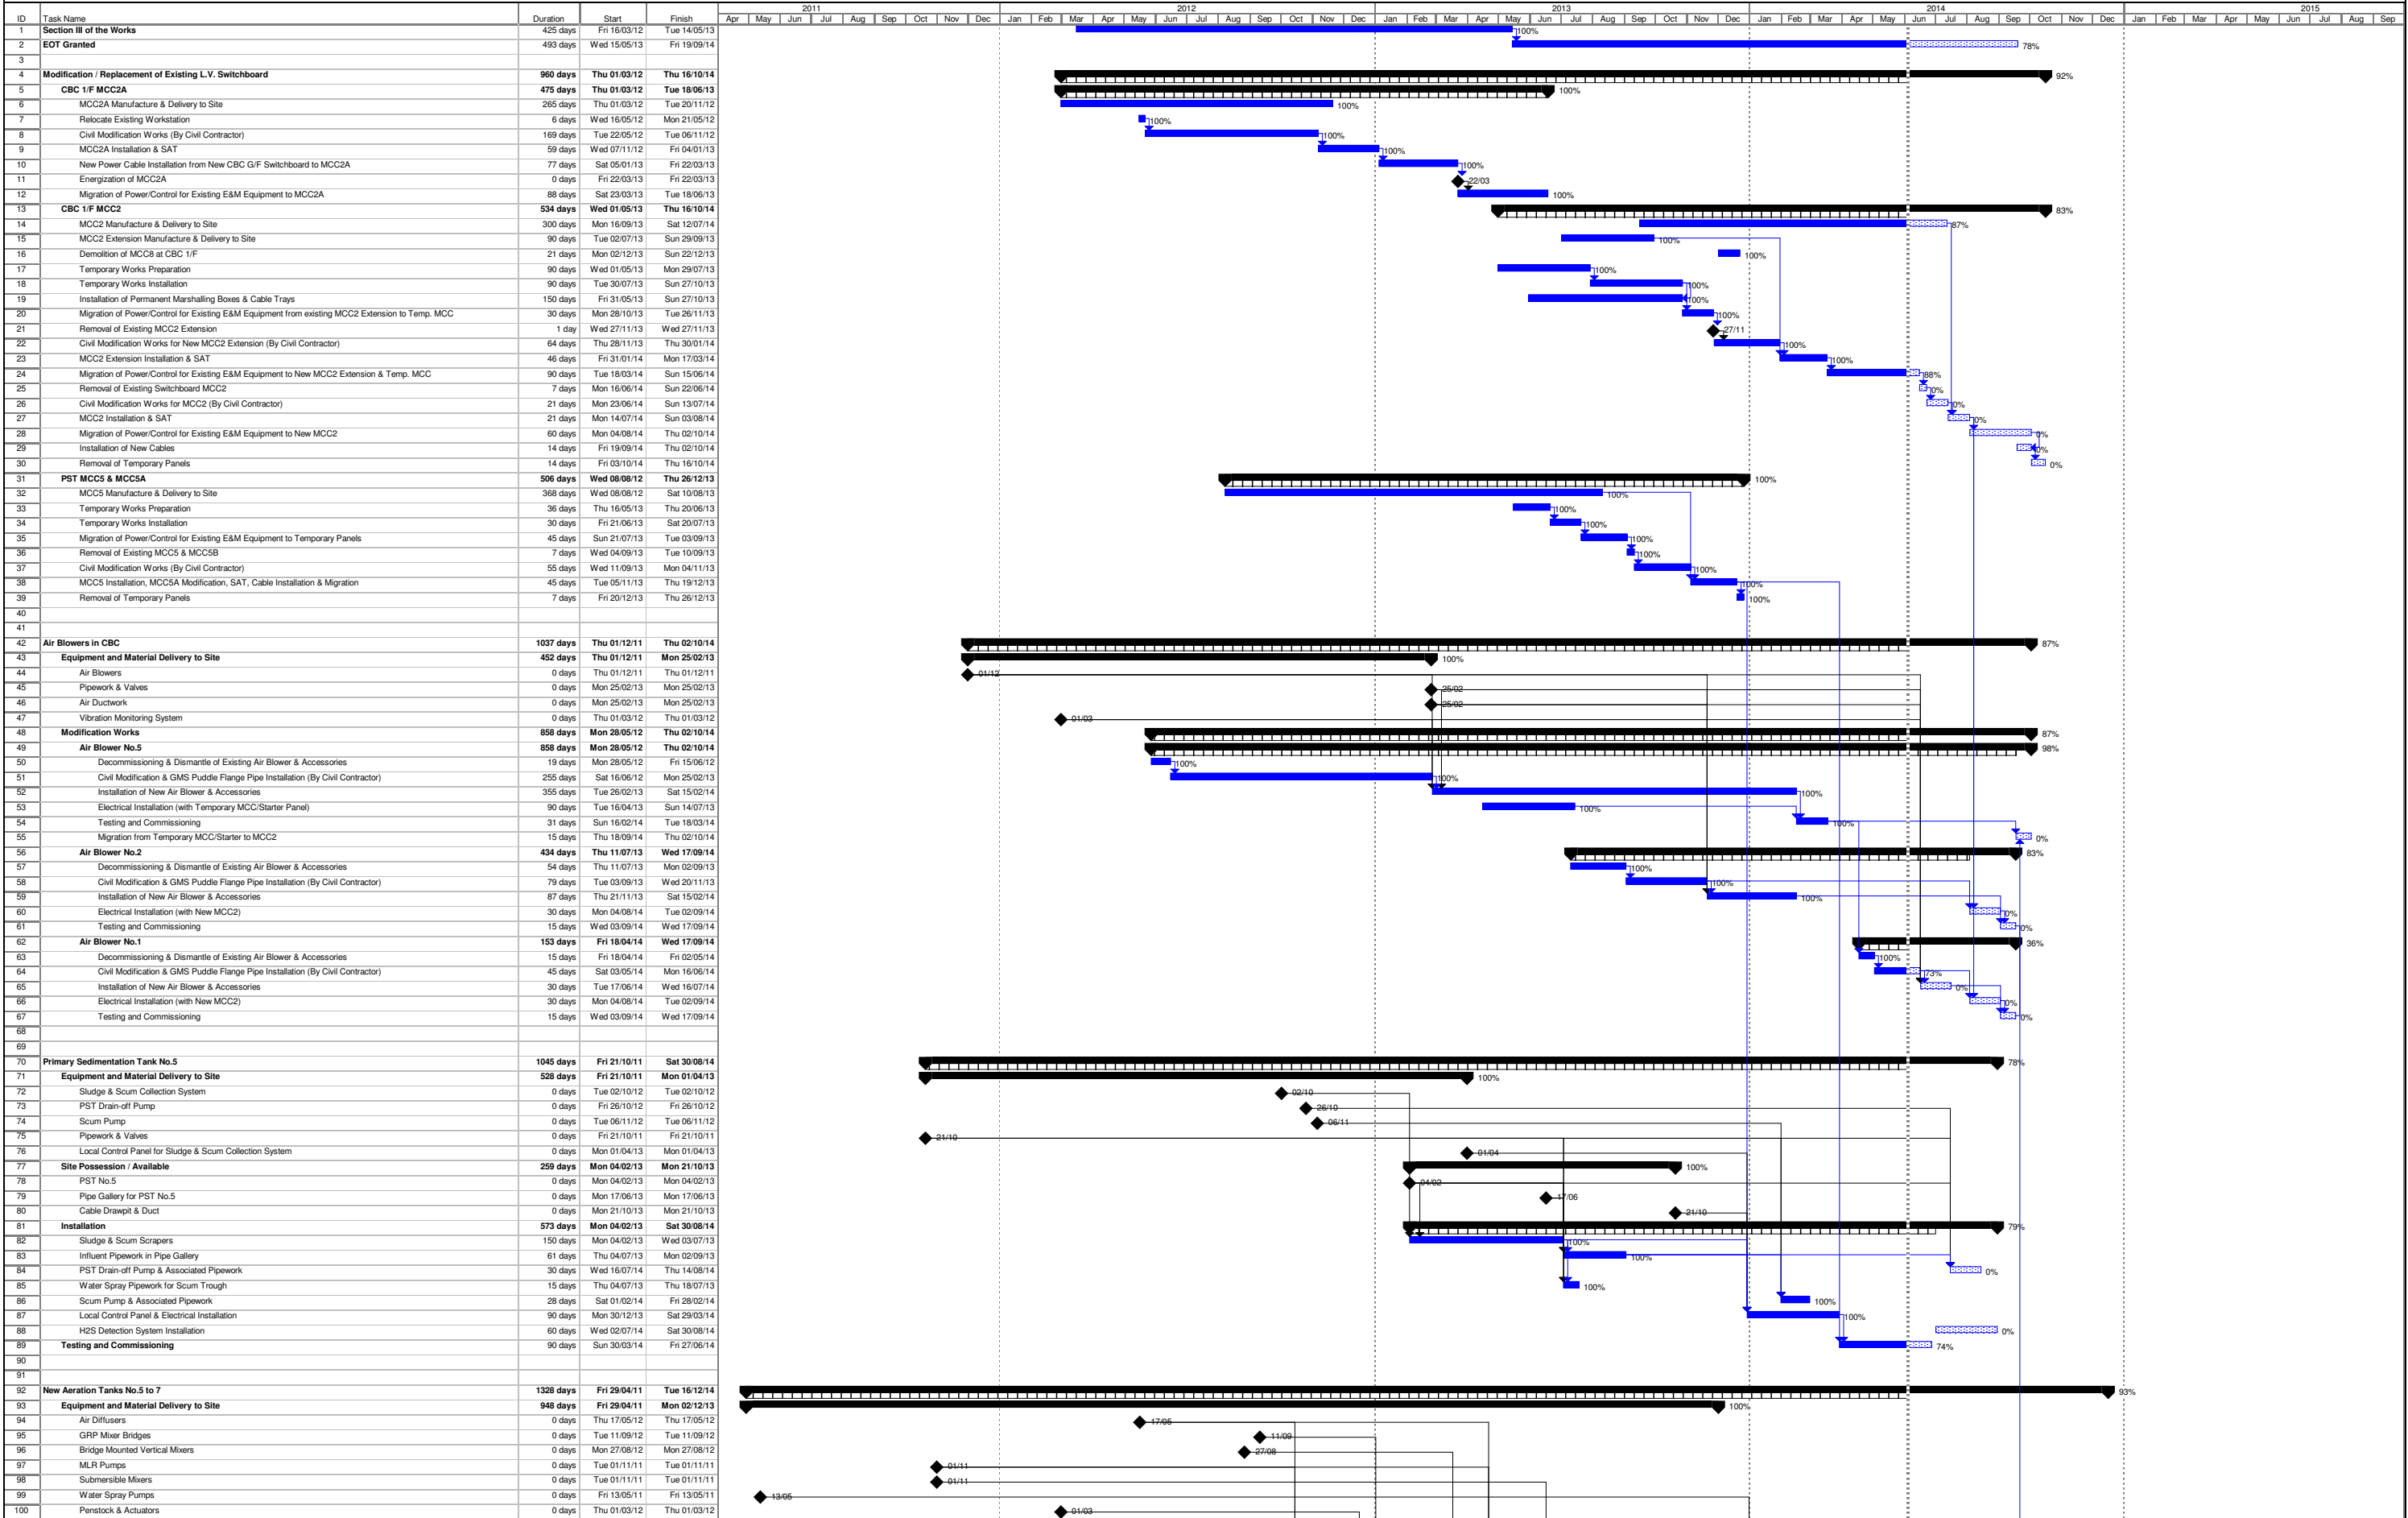



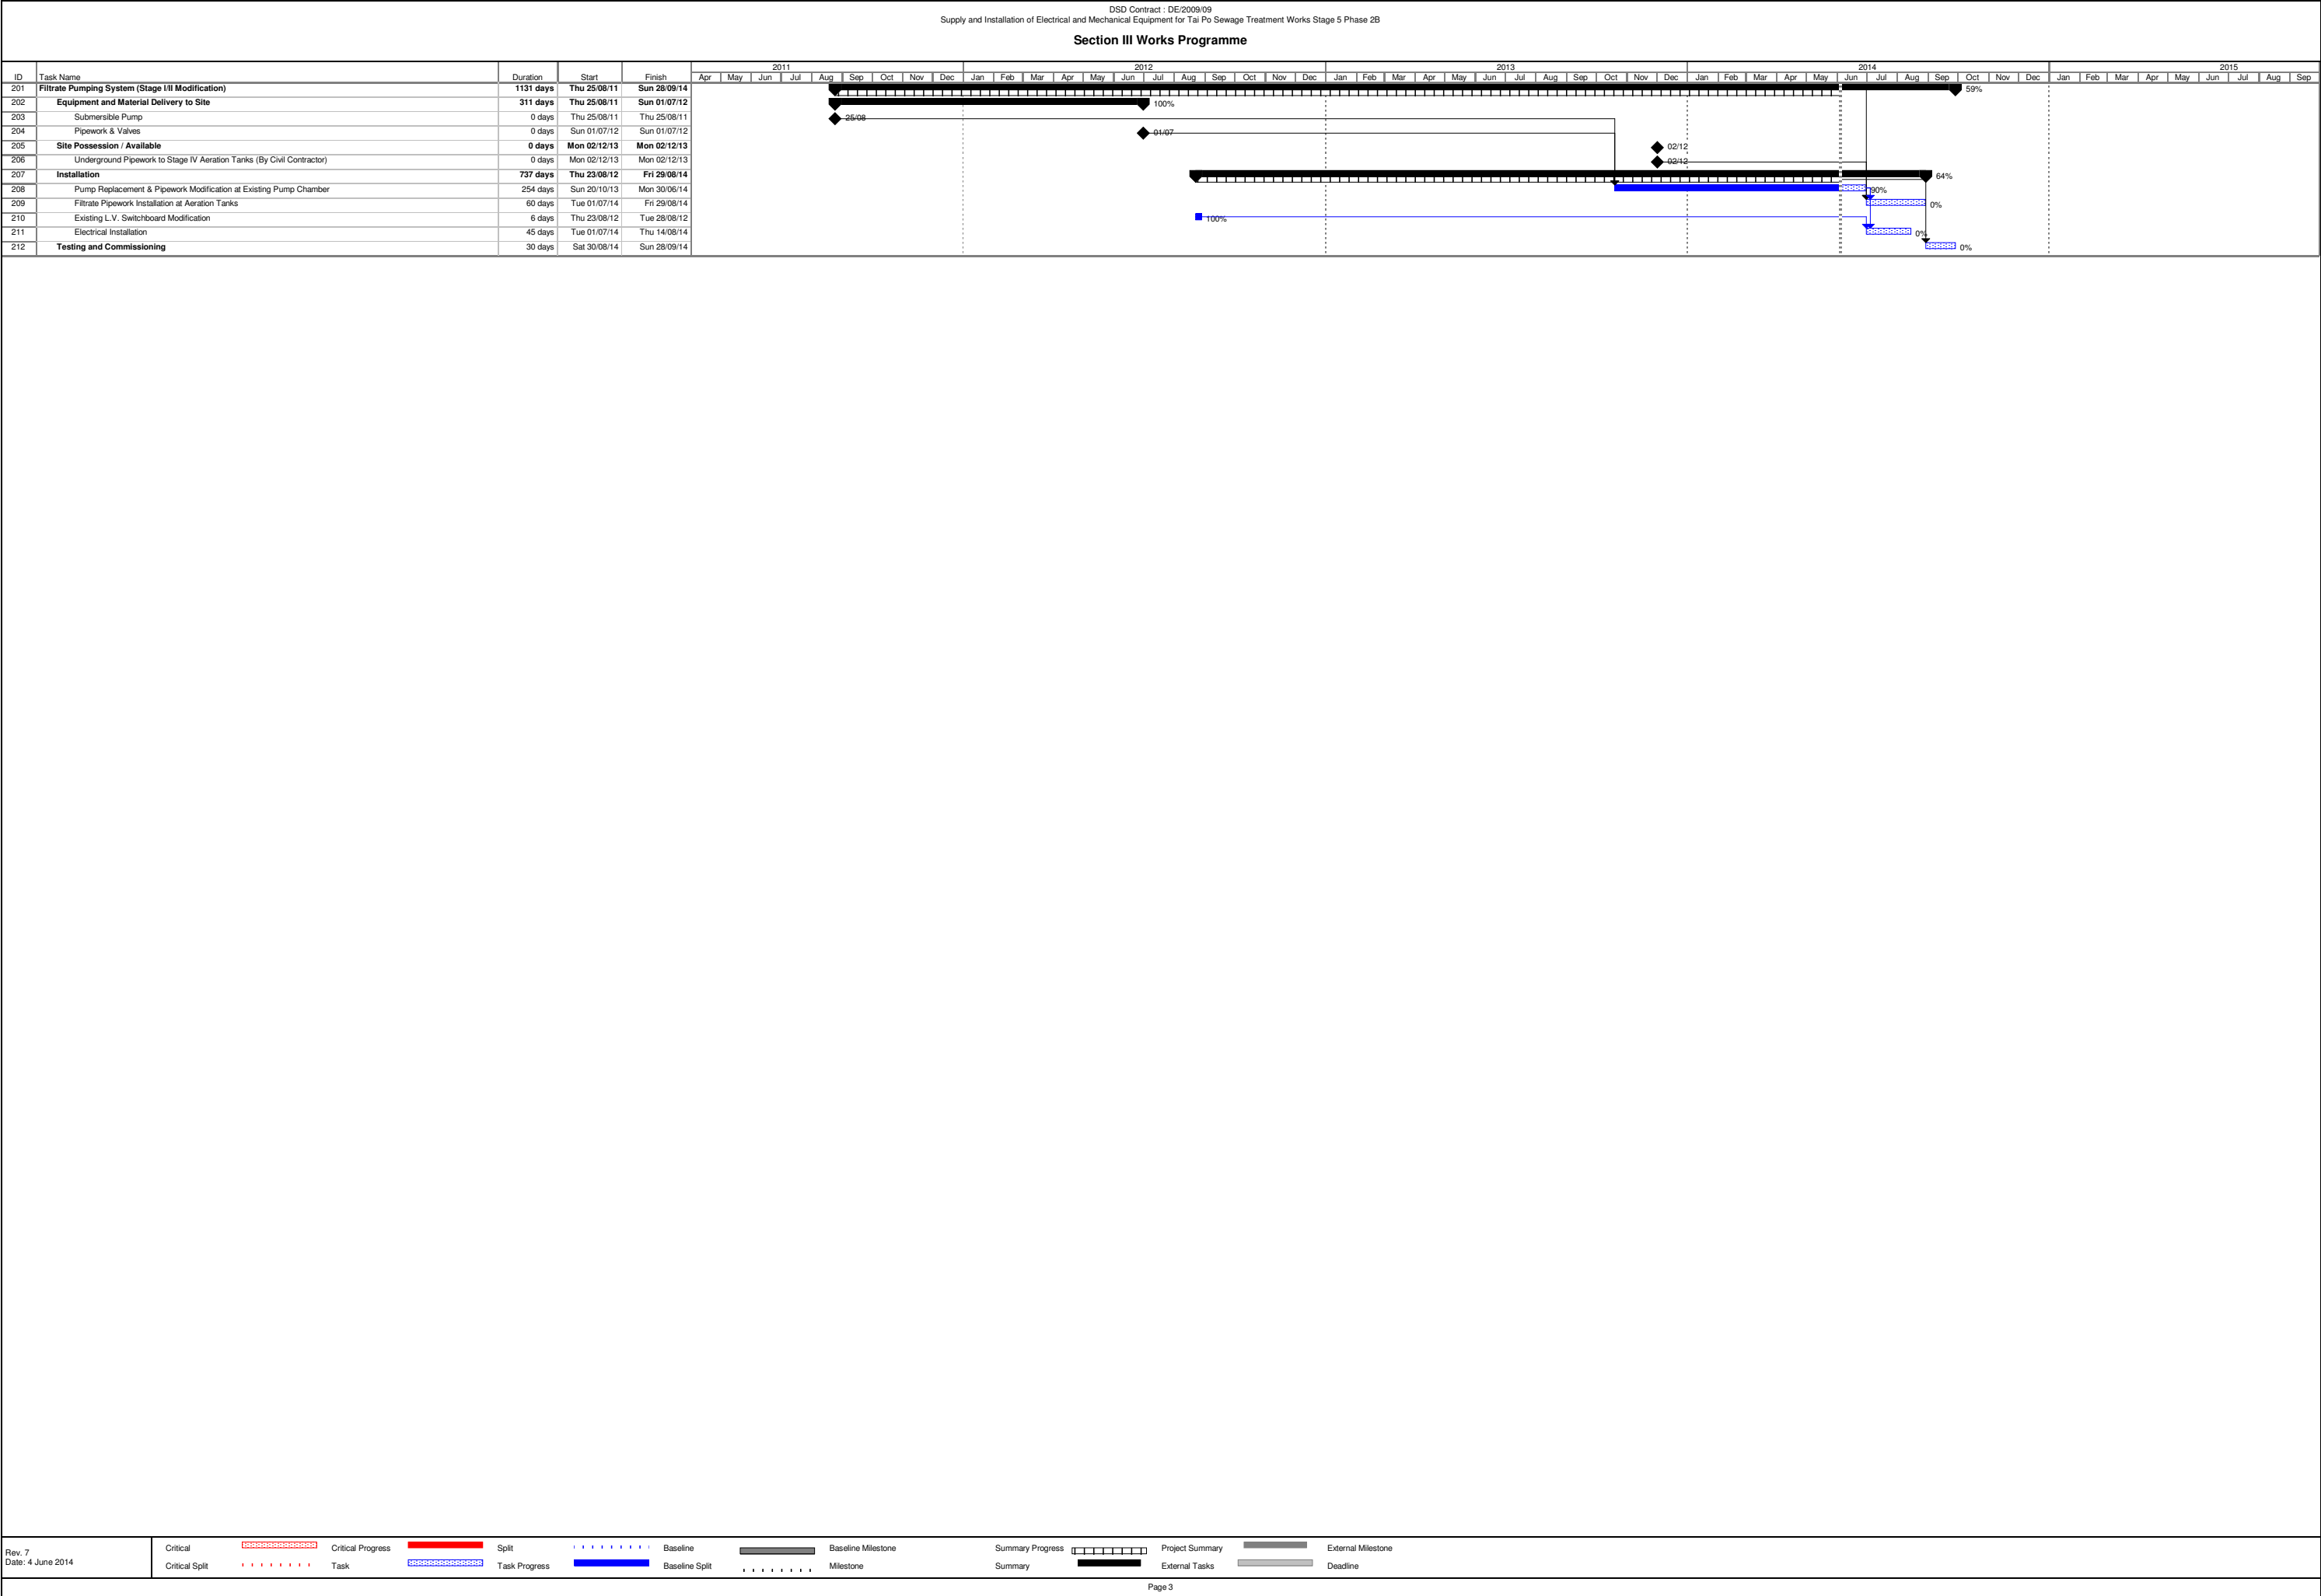

Section V Works Programme

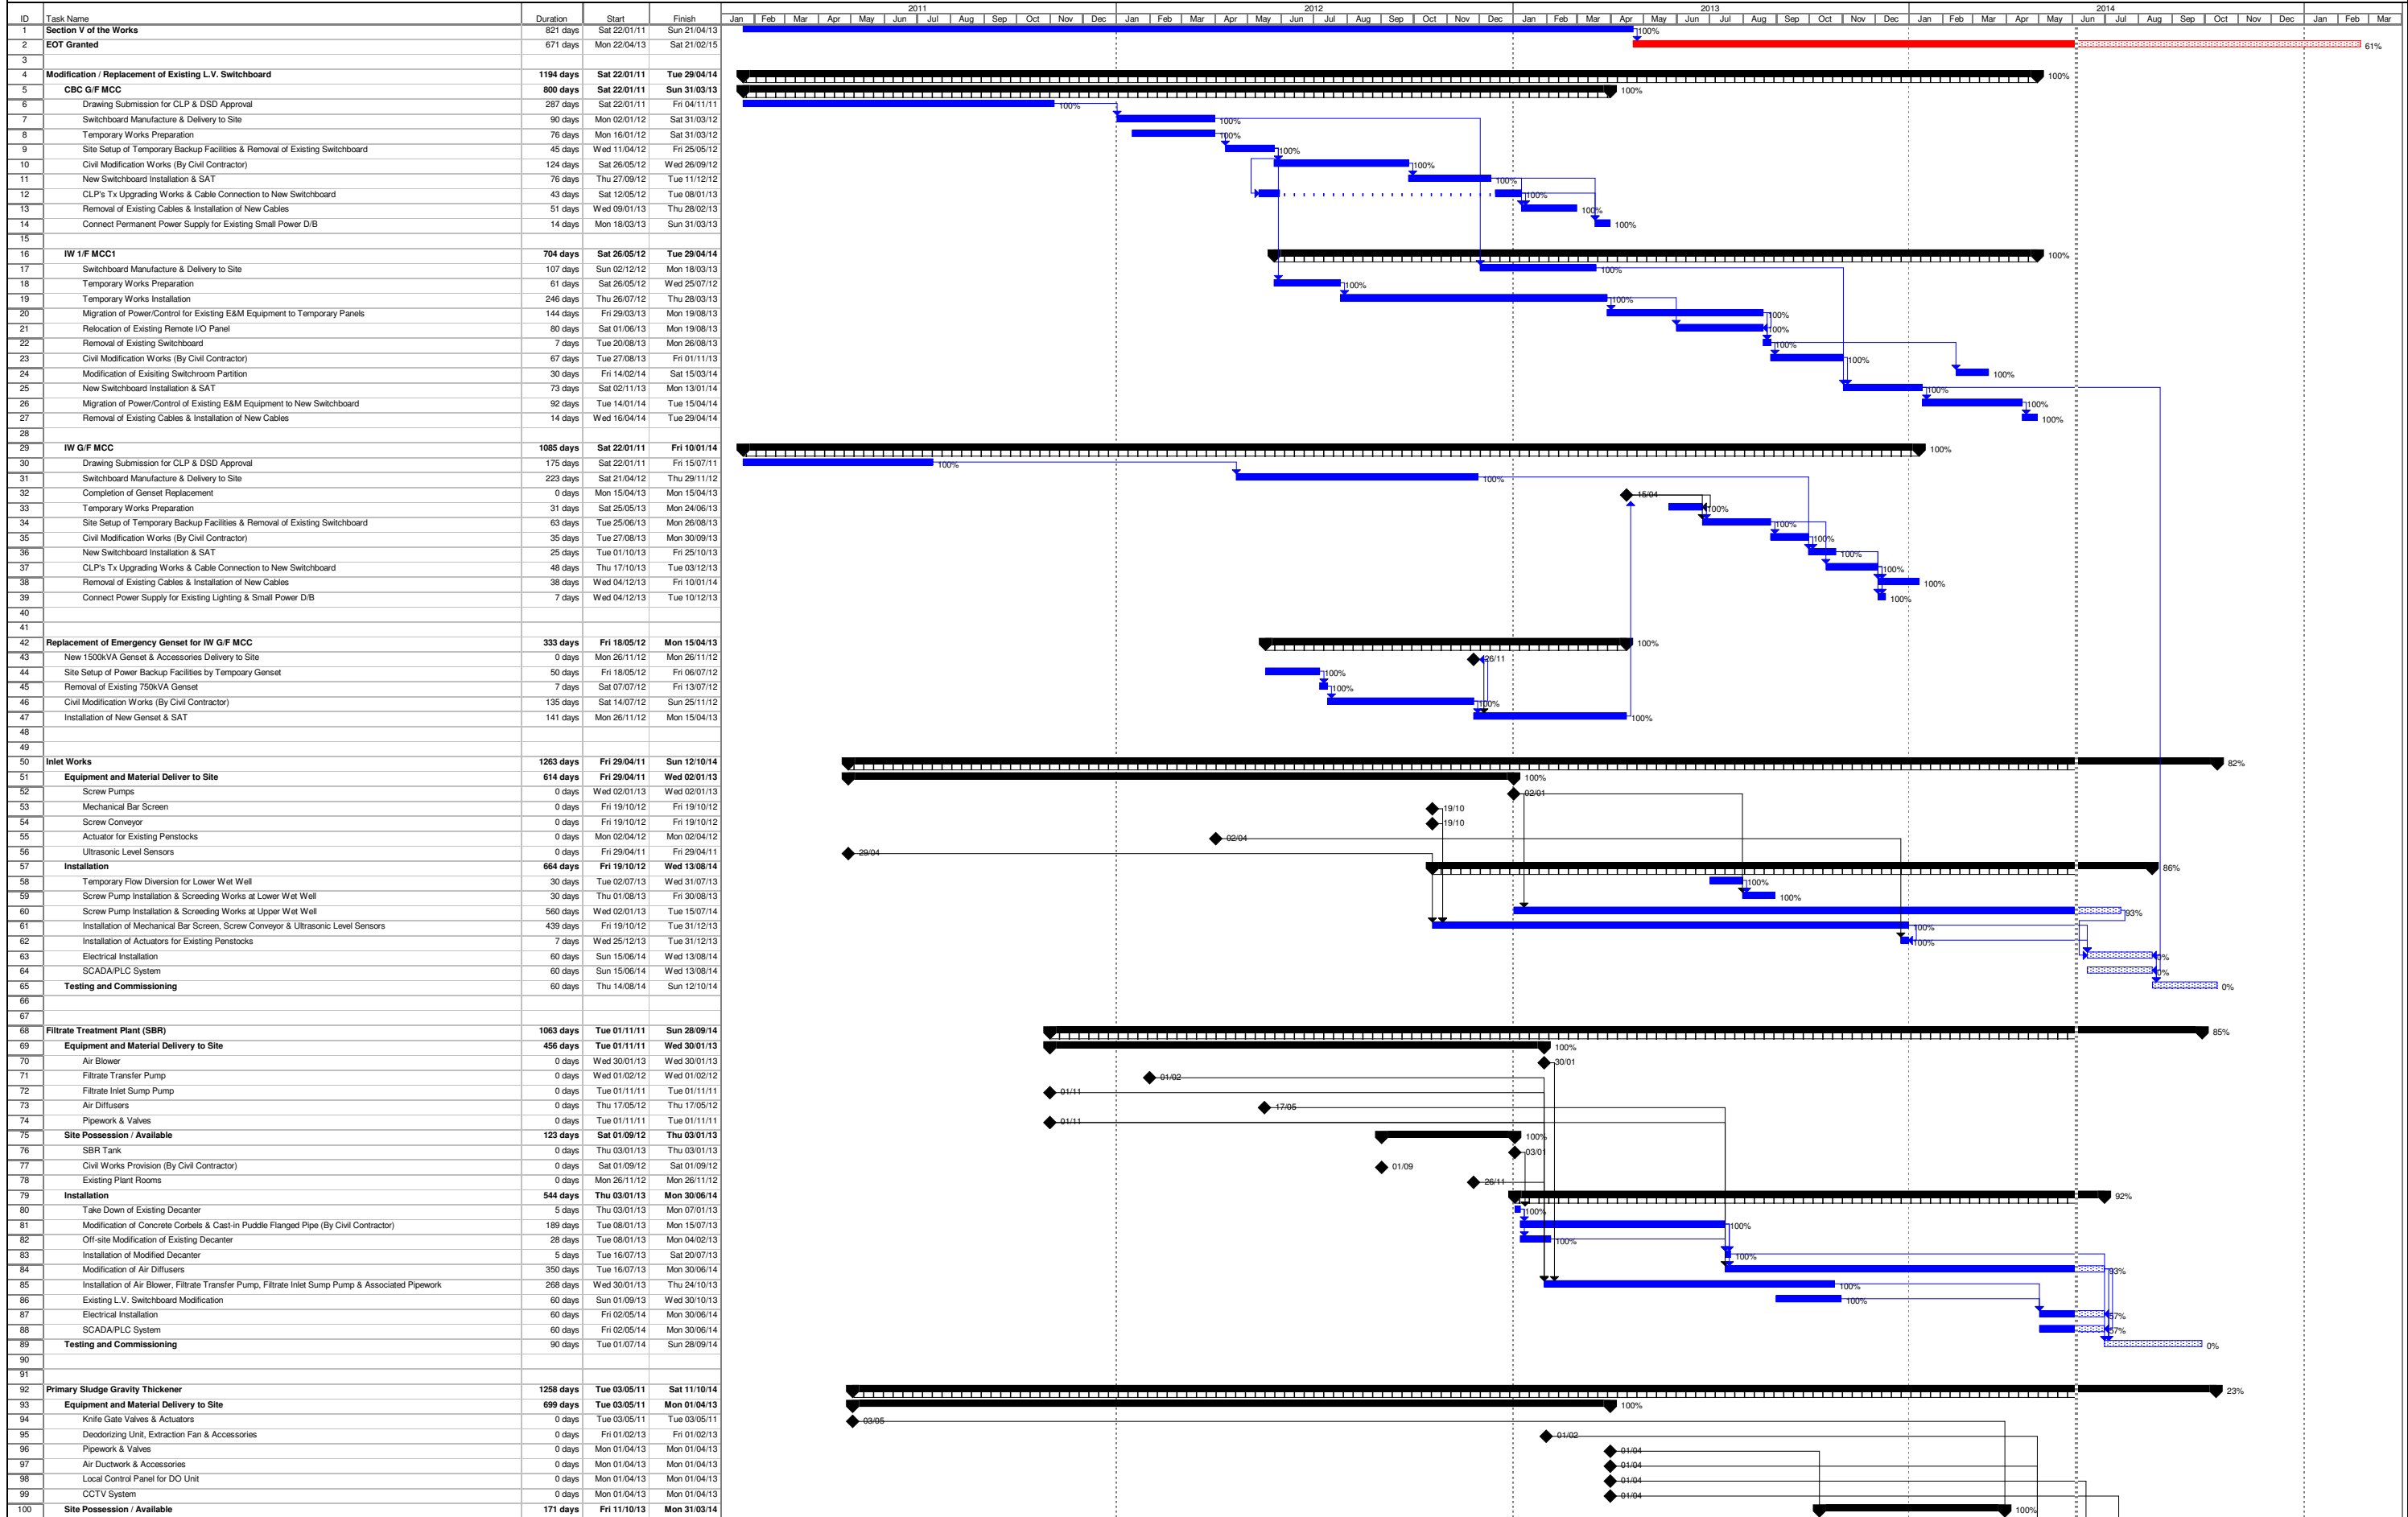

Section V Works Programme

