

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

MONTHLY EM&A REPORT

June 2016

Client : Civil Engineering and Development
Department, HKSAR

Contract No. : KLN/2015/07

Contract Name : Environmental Monitoring Works for
Contract KL/2014/03 – Kai Tak Development
– Stage 3 Infrastructure Works for Developments
at the Southern Part of the Former Runway

Report No. : 0405/15/ED/0507B

EP-337/2009 New Distributor Roads Serving the Planned Kai Tak
Development Area


EP-339/2009/A Decommissioning of the Remaining Parts (Ex-GFS
Building, Radar Station and Hong Kong Aviation Club)
of the former Kai Tak Airport

EP-451/2013 Trunk Road T2

Prepared by : Alfred Y. S. Lam

Reviewed by : Cyrus C. Y. Lai

Certified by :



Colin K. L. Yung
Environmental Team Leader
MaterialLab Consultants Limited

Ref.: CEDKTDS3EM00_0_0089L.16

13 July 2016

Hyder-Meinhardt Joint Venture
20/F., AXA Tower,
Landmark East,
100 How Ming Street,
Kwun Tong,
Kowloon, Hong Kong

By Post and Email

Attention: Mr. Wong W K, Chris

Dear Mr. Wong,

**Re: Contract No. KL/2014/03 – Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway
Monthly EM&A Report for June 2016**

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for June 2016 (Report No. 0405/15/ED/0507B) we received by e-mail on 13 July 2016.

Please be informed that we have no adverse comment on the captioned report. We hereby verify the captioned submission according to Condition 3.3 of EP-337/2009, Condition 3.3 of EP-339/2009/A and Condition 3.4 of EP-451/2013.

Thank you for your attention. Please do not hesitate to contact us should you have any queries.

Yours sincerely,
For and on behalf of
Ramboll Environ Hong Kong Limited



F. C. Tsang
Independent Environmental Checker

c.c.	CEDD	Attn.: Ms. Amy Chu	Fax: 2369 4980
	MateriaLab	Attn.: Mr. Colin K. L. Yung	Fax: 2450 8032
	CRBC	Attn.: Mr. Arnold Chan	Fax: 2283 1689

Q:\Projects\CEDKTDS3EM00\02_Proj_Mgt\02_Corr\CEDKTDS3EM00_0_0089L.16.docx

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

MaterialLab

TABLE OF CONTENTS

EXECUTIVE SUMMARY	I
1. INTRODUCTION	1
2. AIR QUALITY	5
3. NOISE	10
4. LANDSCAPE AND VISUAL	14
5. WASTE MANAGEMENT	15
6. SITE INSPECTION	16
7. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	17
8. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	18
9. FUTURE KEY ISSUES	19
10. CONCLUSIONS	20

FIGURES

Figure 1	Project General Layout
Figure 2	Air and Noise Monitoring Locations

LIST OF APPENDICES

Appendix A	Construction Programme
Appendix B	Project Organization Chart
Appendix C	Action and Limit Levels for Air Quality and Noise
Appendix D	Calibration Certificates of Monitoring Equipment
Appendix E	Environmental Monitoring Schedules
Appendix F	Air Quality Monitoring Data
Appendix G	Noise Monitoring Data
Appendix H	Event Action Plans
Appendix I	Waste Flow Table
Appendix J	Environmental Mitigation Implementation Schedule (EMIS)
Appendix K	Weather and Meteorological Conditions during Reporting Month
Appendix L	Cumulative statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions
Appendix M	Summary of Site Audit in the Reporting Month
Appendix N	Outstanding Issues and Deficiencies

EXECUTIVE SUMMARY

- i. The Civil Engineering and Development Department HKSAR has appointed MaterialLab Consultants Limited (MCL) to undertake the Environmental Team services for the Project and implement the EM&A works.
- ii. This Monthly EM&A report presents the environmental monitoring and audit works for the period between 1 June 2016 and 30 June 2016. As informed by the Contractor, major activities in the reporting month were:
 - Carrying out pre-drilling;
 - Construction of guide walls and D-walls at Zone 2;
 - Construction of H piles at Zone 1, 3 & 4;
 - Demolition of foundation at Zone 4;
 - Construction of temporary utility diversion at Zone 1;
 - Construction of subway B at Zone 1;
 - Implementation of Temporary Traffic Arrangement (TTA) along Cheung Yip Street and Shing Cheong Road;
 - Erection of scaffolding at Radar Tower;
 - Removal of Asbestos materials at Radar Tower; and
 - Construction of temporary road at Zone 4.

Breaches of the Action and Limit Levels

- iii. No Action / Limit Level exceedance was recorded for 24-hr TSP and construction noise at KTD1a, KTD2a and KER1a in the reporting month.

Complaint, Notification of Summons and Successful Prosecution

- iv. No environmental complaint and no notification of summons and successful prosecution were received in the reporting month.

Reporting Changes

- v. There was no reporting change in the reporting month.

Future Key Issues

- vi. The key issues to be considered in the coming reporting month include:

Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality, waste management and landscape and visual impact.

1. INTRODUCTION

1.1 Background

1.1.1 The Kai Tak Development is located in the south-eastern part of Kowloon Peninsula of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling.

1.1.2 Contract No. KL/2014/03 is the works package to construct an approximately 420m long supporting underground structure (SUS) underneath Shing Cheong Road and Cheung Yip Street. The EM&A programme under this Contract is governed by three EPs (EP-337/2009, EP-339/2009/A and EP-451/2013) and two EM&A Manuals (AEIAR-130/2009 and AEIAR-174/2013). The Works to be executed under this Contract and corresponding EPs include but not be limited to the following main items:

EP-451/2013 – Trunk Road T2

(i) Construction of approximately 420m long supporting underground structure (SUS) including diaphragm walls, barrettes, piled foundation, top and bottom slabs, end wall and adits underneath Shing Cheong Road and Cheung Yip Street;

EP-337/2009 – New Distributor Roads Serving the Planned Kai Tak Development

(ii) Widening and re-alignment of Cheung Yip Street of approximately 330m long and associated footpaths;

(iii) Demolition, reconstruction and widening of Shing Cheong Road of approximately 410m long and associated footpaths;

(iv) Construction of drainage outfall and modification of existing seawall;

(v) Construction of ancillary works including surface drainage, sewerage, water, fire fighting, street lighting, street furniture, road marking, road signage, utilities and services, irrigation and landscape works.

EP-339/2009/A – Decommissioning of the Remaining Parts (Ex-GFS Building, Radar Station and Hong Kong Aviation Club) of the former Kai Tak Airport

(vi) Demolition of RADAR Tower and guard house;

Other works not covered by any EP

(vii) Construction of two subways between Phase II of New Acute Hospital (Site A) and Hong Kong Children's Hospital (Site C), and between Phase I of New Acute Hospital (Site B) and Site C;

(viii) Construction of District Cooling System (DCS) along Cheung Yip Street and Shing Cheong Road

1.1.3 The location and boundary of the site is shown in **Figure 1**.

1.1.4 This Monthly EM&A report is required under EP-337/2009 Condition 3.3, EP-339/2009/A Condition 3.3 and EP-451/2013 Condition 3.4. It is to report the results and findings of the EM&A programme required in the EM&A Manuals.

1.1.5 This is the fourth monthly EM&A Report which summaries the impact monitoring results and audit findings for the Project within the period between 1 June 2016 and 30 June 2016.

1.2 Project Organization

1.2.1 The project proponent was the Civil Engineering and Development Department, HKSAR (CEDD). Hyder Meinhardt Joint Venture (HMJV) was commissioned by CEDD as the Engineer for the Project. Ramboll Environ Hong Kong Limited was commissioned as the Independent Environmental Checker (IEC). China Road and Bridge Corporation (Hong Kong) (CRBC) was appointed as the main contractor for the construction works under the contract KL/2014/03. MaterialLab Consultants Limited (MCL) was appointed as the Environmental Team (ET) by CEDD to implement the EM&A programme for the Project.

1.2.2 The organization structure is shown in **Appendix B**. The key personnel contact names and numbers for the Project are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Project Proponent (CEDD)	Co-ordinator	Ms. Amy Chu	3106 3172	2369 4980
Engineer's Representative (HMJV)	Chief Resident Engineer	Mr. W. K., Chris Wong	2911 2233	2805 5028
IEC (Ramboll Environ Hong Kong Limited)	Independent Environmental Checker	Mr. F. C. Tsang	3465 2888	3465 2899
Main Contractor (CRBC)	Site Agent	Mr. Chan See Wai, Arnold	9380 4110	2283 1689
	Environmental Officer	Mr. Wong Tan Tat	9492 5918	2283 1689
ET (MCL)	Environmental Team Leader	Mr. Colin Yung	3565 4114	3565 4160

1.3 Construction Programme and Activities

1.3.1 The construction of the Project commenced in February 2016 and is expected to complete in 2020. The construction programme is shown in **Appendix A**.

1.3.2 A summary of the major construction activities undertaken in the reporting month were:

- Carrying out pre-drilling;
- Construction of guide walls and D-walls at Zone 2;
- Construction of H piles at Zone 1, 3 & 4;
- Demolition of foundation at Zone 4;
- Construction of temporary utility diversion at Zone 1;
- Construction of subway B at Zone 1;
- Implementation of Temporary Traffic Arrangement (TTA) along Cheung Yip Street and Shing Cheong Road;
- Erection of scaffolding at Radar Tower;
- Removal of Asbestos materials at Radar Tower; and
- Construction of temporary road at Zone 4.

1.4 Inter-relationship with the environmental protection/ mitigation measures with the construction programme

1.4.1 According to the construction activities in the construction programme mentioned in Section 1.3.2, the following environmental protection/ mitigation measures including Air Quality Impact, Construction Noise Impact, Water Quality Impact, Chemical and Waste Management, Landscape and Visual Impact shall be implemented:

- Sufficient watering of the works site with the active dust emitting activities;
- Limitation of the speed for vehicles on unpaved site roads;
- Properly cover or enclosure of the stockpiles and dusty materials;
- Good site practices on loading dusty materials;
- Providing sufficient vehicles washing facilities at every vehicle exit point;
- Good maintenance to the plant and equipment;
- Use of quieter plant and Quality Powered Mechanical Equipment (QPME);
- Use of acoustic fabric and noise barrier;
- Using the approved Non-road Mobile Machineries (NRMMS);
- Proper storage and handling of chemical;
- Appropriate desilting, oil interceptors or sedimentation devices provided on site for treatment before discharge;
- Onsite waste sorting and implementation of trip ticket system;
- Training of the site personnel in proper waste management and chemical waste handling procedures;
- Proper storage of the construction materials;
- Erection of decorative screen hoarding;
- Strictly following the Environmental Permits and Licenses;
- Provide sufficient mitigation measures as recommended in Approved EIA Reports

1.5 Status of Environmental Licences, Notifications and Permits

1.5.1 A summary of the relevant environmental licenses, permits and/or notifications on environmental protection for this Contract is presented in **Table 1.2**.

Table 1.2 Relevant Environmental Licenses, Permits and/or Notifications

Environmental License / Permit / Notification	Reference Number	Valid From	Valid Till
Environmental Permit	EP-337/2009 EP-339/2009/A EP-451/2013	23 April 2009 18 June 2009 19 September 2013	Not Applicable Not Applicable Not Applicable
Notification pursuant to Air Pollution (Construction Dust) Regulation	395601	16 November 2015	Not Applicable
Billing Account for Waste Disposal	A/C No.: 7023814	30 November 2015	Not Applicable
Construction Noise Permit	GW-RE0538-16	1 June 2016	30 November 2016
Construction Noise Permit	PP-RE0013-16	16 May 2016	15 November 2016
Wastewater Discharge License	WT00023125-2015	6 January 2016	31 January 2021
Chemical Waste Producer License	5213-247-C1232-12	23 November 2015	Not Applicable

2. AIR QUALITY

2.1 Monitoring Requirement

In accordance with the approved EM&A Manuals, 24-hour Total Suspended Particulates (TSP) level at the designated air quality monitoring station is required. Impact 24-hour TSP monitoring should be carried out at least once every 6 days. In case of complaints, 1-hour TSP monitoring should be carried out at least 3 times per 6 days when the highest dust impacts are likely to occur. The Action and Limit Levels of the air quality monitoring are given in **Appendix C**.

2.2 Monitoring Equipment

The 24-hour TSP air quality monitoring was performed using High Volume Air Samplers (HVS) located at each of the designated monitoring station. Portable TSP Monitors would be used in case of complaints for 1-hour TSP monitoring.

Table 2.1 summarizes the equipment used in air quality monitoring.

Table 2.1 Air Quality Monitoring Equipment

Item	Brand	Model	Equipment	Serial Number
1	Tisch	TE-5170 (TSP)	High Volume Sampler	
		TE-300-310X	- Mass Flow Controller	2037
		TE-5005X	- Blower Motor Assembly	3482
		TE-5007X	- Mechanical Timer	4488
		TE-5009X	- Continuous Flow Recorder	4371
2	Tisch	TE-5170 (TSP)	High Volume Sampler	
		TE-300-310X	- Mass Flow Controller	2364
		TE-5005X	- Blower Motor Assembly	3478
		TE-5007X	- Mechanical Timer	4492
		TE-5009X	- Continuous Flow Recorder	4377
3	Tisch	TE-5170 (TSP)	High Volume Sampler	
		TE-300-310X	- Mass Flow Controller	2618
		TE-5005X	- Blower Motor Assembly	3838
		G3031	- Mechanical Timer	2251
		G1051	- Continuous Flow Recorder	2307
4	Tisch	TE-5025A	HVS Sampler Calibrator	0438320 / 2154 0428320 / 2456
5	*Sibata	Model LD-3B	Sibata Portable TSP Monitors	NA

Note:

No complaint of air quality was received. Therefore, no impact 1-hour TSP monitoring was conducted.

2.3 Monitoring Methodology

2.3.1 24-hour TSP air quality monitoring

HVS Installation

The following guidelines were adopted during the installation of HVS:

- Sufficient support is provided to secure the samplers against gusty wind.
- No two samplers are placed less than 2 meters apart.

- The distance between the sampler and an obstacle, such as buildings, is at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2 meters of separation from walls, parapets and penthouses is required for rooftop samples.
- A minimum of 2 meters separation from any supporting structure, measured horizontally is required.
- No furnaces or incineration flues are nearby.
- Airflow around the samplers is unrestricted.
- The samplers are more than 20 meters from the drip line.
- Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.

Filters Preparation

Fiberglass filters (provided by the HOKLAS accredited laboratory) shall be used (Note: these filters have a collection efficiency of larger than 99% for particles of 0.3 μm diameter). A HOKLAS accredited laboratory (ALS Technichem (HK) Pty Ltd.) is responsible for the preparation of 24-hr conditioned and pre-weighed filter papers for monitoring team.

All filters are equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature is around 25°C and not variable by more than $\pm 3^\circ\text{C}$; the relative humidity (RH) is < 50% and not variable by more than $\pm 5\%$. A convenient working RH is 40%.

Operating / Analytical Procedures

Operating / analytical procedures for the air quality monitoring are highlighted as follows:

- Prior to the commencement of the dust sampling, the flow rate of the HVS are properly set (between 1.1 m^3/min . and 1.4 m^3/min .) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. The flow rate shall be indicated on the flow rate chart.
- The power supply shall be checked to ensure the samplers worked properly.
- On sampling, the samplers shall be operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air quality monitoring station.
- The filter holding frame is then removed by loosening the four nuts and carefully a weighted and conditioned filter is centered with the stamped number upwards, on a supporting screen.
- The filter shall be aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame is tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The shelter lid shall be closed and secured with the aluminum strip.
- The timer is then programmed. Information shall be recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- After sampling, the filter shall be removed and sent to laboratory for weighing. The elapsed time is also recorded.
- Before weighing, all filters are equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than $\pm 3^\circ\text{C}$; the relative humidity (RH) should be < 50% and not vary by more than $\pm 5\%$. A convenient working RH is 40%. Weighing results are returned to MCL for further analysis of TSP concentrations collected by each filter.

2.3.2 1-hour TSP air quality monitoring

Operating / Analytical Procedures

The measuring procedures of the 1-hr dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Pull up the air sampling inlet cover
- Change the Mode 0 to BG once
- Push Start/Stop switch once
- Turn the knob to SENSI.ADJ and press it
- Push Start/Stop switch once
- Return the knob to the position MEASURE slowly
- Push the timer set switch to set measuring time
- Remove the cap and make a measurement

2.4 Maintenance / Calibration

2.4.1 24-hour TSP air quality monitoring

The following maintenance / calibration are required for the HVS:

- The high volume motors and their accessories are properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking are made to ensure that the equipments and necessary power supply are in good working condition.
- All HVS shall be calibrated (five point calibration) using Calibration Kit upon installation and thereafter in every 3 months.
- A copy of the calibration certificates for the HVS and calibrator are provided in **Appendix D**.

2.4.2 1-hour TSP air quality monitoring

The portable TSP monitor should be calibrated at 1 year intervals

2.5 Monitoring Locations

2.5.1 According to the EM&A Manual, three air quality monitoring locations, namely KTD1, KTD2 and KER1, are covered by this Contract within the South Apron Area of Former Kai Tak Airport. The other two air quality monitoring locations, which are identified in Cha Kwo Ling area, are farther than 500m away from the site boundary and thus not covered by this Contract. The monitoring works in Cha Kwo Ling area are covered by other Contract(s) respectively.

2.5.2 According to the approved alternative baseline air quality and noise monitoring locations (EPD reference: EP2/K19/A/21 Pt.5), the original monitoring locations (KTD1, KTD2 and KER1) are proposed to be replaced by alternative monitoring locations (KTD1a, KTD2a and KER1a) for air quality monitoring, they are summarized in **Table 2.2** and shown in **Figure 2**.

Table 2.2 Location of Air Quality Monitoring Station

Monitoring Station	Location
KTD1a	Centre of Excellence in Paediatrics (Children’s Hospital)
KTD2a	G/IC Zone next to Kwun Tong Bypass (Future Hospital at Site 3C1)
KER1a	Site Boundary at Cheung Yip Street

2.6 Results and Observations

- 2.6.1 The schedule of air quality monitoring in reporting month is provided in **Appendix E**.
- 2.6.2 No Action / Limit Level exceedance was recorded for 24-hr TSP at KTD1a, KTD2a and KER1a in the reporting month.
- 2.6.3 No complaint of air quality was received. Therefore, no impact 1-hour TSP monitoring was conducted in the reporting month.
- 2.6.4 During the reporting month, major dust sources including loading and unloading of C&D wastes, vehicles movement were observed in the site. Non-project related construction activities at the nearby construction site and road traffic along Shing Cheong Road, Cheung Yip Street and the Kwun Tong By-pass were observed. The above factors may affect the monitoring results.
- 2.6.5 The weather conditions during the monitoring are provided in **Appendix K**.
- 2.6.6 The monitoring data of 24-hr TSP are summarized in **Table 2.3**. Detailed monitoring data are presented in **Appendix F**.

Table 2.3 Summary of 24-hr TSP Monitoring Results

Parameter	Monitoring Station	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
24-hr TSP in $\mu\text{g}/\text{m}^3$	KTD1a	79	46 – 146	177	260
	KTD2a	51	39 – 66	157	
	KER1a	38	19 – 59	172	

- 2.6.7 The Event and Action Plan for air quality is given in **Appendix H**.

2.7 Comparison of 24-hr TSP Monitoring Results with EIA Predictions

- 2.7.1 The monitoring data of 24-hr TSP was compared with the EIA predictions as summarized in **Table 2.4**.

Table 2.4 Comparison of 24-hr TSP data with EIA predictions

Monitoring Station	Receiver Reference	Predicted Maximum 24-hour TSP Concentration ($\mu\text{g}/\text{m}^3$)	24-hour TSP concentration in June 2016 ($\mu\text{g}/\text{m}^3$)	Average 24-hour TSP concentration in June 2016 ($\mu\text{g}/\text{m}^3$)
KTD1a	KTD3	126	46 – 146	79
KTD2a	-	-	39 – 66	51
KER1a	KTD6	169	19 – 59	38

Note:

For KTD2a, there was no receiver reference in the EIA report, EIAR-174/2013.

Predicted Maximum TSP Concentration extracted from Table 4.14 of EIA Report, EIAR-174/2013.

- 2.7.2 The 24-hour TSP monitoring results of KER1a were below the Predicted Maximum 24-hour TSP concentration in the approved Environmental Impact Assessment (EIA) Report.
- 2.7.3 The 24-hour TSP monitoring result of KTD1a on 25 June 2016 was $146 \mu\text{g}/\text{m}^3$, which exceeded the prediction in the approved EIA report. However, the result did not exceed the Action Level. Mitigation measures, including water spraying and covering of stockpiles of dusty materials were adopted and observed during the site inspection on 23 June 2016 and 30 June 2016. The discrepancy between the 24-hour TSP concentration and EIA Prediction in KTD1a is considered due to dust source from the non-project related construction activities near the monitoring station and the road travel along Shing Fung Road.

3. NOISE

3.1 Monitoring Requirement

In accordance with the approved EM&A Manuals, Leq (30min) monitoring is conducted for at least once a week during the construction phase between 0700 and 1900 on normal weekdays at the designated monitoring locations.

3.2 Monitoring Equipment

The sound level meter used in noise monitoring will comply with the International Electrotechnical Commission Publication (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum issued under the Noise Control Ordinance (NCO).

Sound level calibrator will be used for the on-site calibration of the meter. This calibrator complies with the IEC Publication 942 (1988) Class 1 and ANSI S1.40 - 1984. Noise measurements were only accepted to be valid if the calibration levels from before and after the measurement agree to within 1.0dB.

Measurements shall be recorded to the nearest 0.1dB. This noise monitors are programmed to measure A-weighted equivalent continuous sound pressure level at 30-minute intervals between 0700 and 1900 on normal weekdays at least once a week when construction activities are underway.

Table 3.1 summarizes the noise monitoring equipment model being used for this project.

Table 3.1 Noise Monitoring Equipment

Item	Brand	Model	Equipment	Serial Number
1	Casella	CEL-63X Series	Integrating Sound Level Meter	3321823
2	Casella	CEL-63X Series	Integrating Sound Level Meter	3756084
3	Casella	CEL-63X Series	Integrating Sound Level Meter	3756127
4	Casella	CEL-120/1	Calibrator	5230736
5	Casella	CEL-120/1	Calibrator	5230742
6	Casella	CEL-120/1	Calibrator	4358251
7	Smart Sensor	AR816+	Wind Speed Anemometer	NA

3.3 Monitoring Parameters and Frequency

Table 3.2 presents the noise monitoring parameters and frequencies.

Table 3.2 Monitoring Parameters and Frequencies of Noise Monitoring

Parameter	Frequency and Period
LAeq (30min) L10 and L90 will be recorded for reference	At each station at 0700-1900 hours on normal weekdays at a frequency of once a week

3.4 Monitoring Methodology

The monitoring procedures are as follows:

- The monitoring station is set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 1.2m above the ground.
- The battery condition is checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time are set as follows:
 - frequency weighting : A
 - time weighting : Fast
 - measurement time : Weekly 30 minutes between 0700-1900 on normal weekdays
- Prior to and after noise measurement, the meter shall be calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement will be considered invalid and repeat of noise measurement is required after re-calibration or repair of the equipment.
- Noise monitoring should be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.
- Noise measurement should be paused during periods of high intrusive noise if possible and observation shall be recorded when intrusive noise is not avoided.
- At the end of the monitoring period, the Leq, L10 and L90 are recorded. In addition, site conditions and noise sources are recorded on a standard record sheet.

3.5 Maintenance / Calibration

Maintenance and Calibration procedures are as follows:

- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory.
- Relevant calibration certificates are provided in **Appendix D**.

3.6 Monitoring Locations

- 3.6.1 According to the EM&A Manual, three noise monitoring locations, namely KTD1, KTD2 and KER1, are covered by this Contract within the South Apron Area of Former Kai Tak Airport. The other two noise quality monitoring locations, which are identified in Cha Kwo Ling area, are farther than 300m away from the site boundary and thus not covered by this Contract. The monitoring works in Cha Kwo Ling area are covered by other Contract(s) respectively.
- 3.6.2 According to the approved alternative baseline air quality and noise monitoring locations (EPD reference: EP2/K19/A/21 Pt.5), the original monitoring locations (KTD1, KTD2 and KER1) are proposed to be replaced by alternative monitoring locations (KTD1a, KTD2a and KER1a) for noise monitoring, they are summarized in **Table 3.3** and shown in **Figure 2**.

Table 3.3 Location of Noise Monitoring Station

Monitoring Station	Location
KTD1a	Centre of Excellence in Paediatrics (Children’s Hospital)
KTD2a	G/IC Zone next to Kwun Tong Bypass (Future Hospital at Site 3C1)
KER1a	Site Boundary at Cheung Yip Street

3.7 Results and Observations

- 3.7.1 The schedule of noise monitoring in reporting month is provided in **Appendix E**.
- 3.7.2 During the monitoring month, at KTD1a, non-project related construction activities at the nearby construction site and road traffic along Shing Cheong Road were observed in the surroundings. At KTD2a, road traffic along the Kwun Tong By-pass was observed. At KER1a, road traffic along Cheung Yip Street was observed. Major noise sources including noise emission from plant & PME and some other construction activities, travel of vehicles, loading and unloading of C&D waste were observed in the site. The above factors may affect the monitoring results.
- 3.7.3 No raining and wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation. The weather conditions during the monitoring month are provided in **Appendix K**.
- 3.7.4 The noise monitoring data are summarized in **Table 3.4**. Detailed monitoring data are presented in **Appendix G**.

Table 3.4 Summary of Noise Impact Monitoring Results

Time Period	Leq (30min) dB(A) (Range)			Action Level	Limit Level
	Noise Monitoring Stations				
	KTD1a	KTD2a	KER1a		
0700-1900 hrs on normal weekdays	60 - 72	59 - 63	67 - 70	When one documented complaint is received	75 dB(A)

Note:

KTD1a: Façade Measurement

KTD2a & KER1a: Free-field measurement (+3dB(A) correction has been applied)

- 3.7.5 No Action / Limit Level exceedance was recorded for construction noise in the reporting month.
- 3.7.6 The Action and Limit Levels for noise impact monitoring have been set are presented in **Appendix C**.
- 3.7.7 The Event and Action Plan for noise is given in **Appendix H**.

3.8 Comparison of Noise Monitoring Results with EIA Predictions

- 3.8.1 The noise monitoring data was compared with the EIA predictions as summarized in **Table 3.5**.

Table 3.5 Comparison of Noise Monitoring data with EIA predictions

Monitoring Station	Receiver Reference	Maximum Predicted Mitigated Construction Noise Level, dB(A)	Leq_(30min) dB(A) in June 2016
KTD1a	KTD1	74	60 - 72
KTD2a	KTD2	75	59 - 63
KER1a	KER1	75	67 - 70

Note:

Maximum Predicted Mitigated Construction Noise Level extracted from Table 5.13 of EIA Report, EIAR-174/2013.

- 3.8.2 The impact noise monitoring results in the reporting month were below the Maximum Predicted Mitigated Construction Noise Level in the approved Environmental Impact Assessment (EIA) Report and no Action / Limit Level exceedance was recorded in the reporting period.

4. LANDSCAPE AND VISUAL

4.1 Audit Requirements

4.1.1 As per the Trunk Road T2 EM&A Manual, the landscape and visual mitigation measures during the construction phase shall be audited by a Registered Landscape Architect, as a member of the Environmental Team, at least once every two weeks to ensure compliance with the intended aims of the measures.

4.1.2 According to the Kai Tak Development EM&A Manual, measures to mitigate landscape and visual impacts during construction should be checked to ensure compliance with the intended aims of the measures. The progress of the engineering works shall be regularly reviewed onsite to identify the earliest practical opportunities for the landscape works to be undertaken. The ET shall report on the Contractor's compliance on a weekly basis.

4.2 Results and Observations

4.2.1 To monitor and audit the implementation of landscape and visual mitigation measures, five weekly Landscape and Visual Site audits were carried out on 2, 8, 15, 23 and 30 June 2016 and three of them, 2, 15 and 23 June 2016 were carried out by a Registered Landscape Architect. The weekly Landscape and Visual Impact reports were counter-signed by IEC as according to the requirement of EM&A Manual (AEIAR-130/2009).

4.2.2 During the Site audit on 2 June 2016, it is observed that open stockpiles at Portion Q were not fully covered. The item was rectified by the Contractor and inspected on 8 June 2016.

4.2.3 Should non-compliance of the landscape and visual impact occur, action in accordance to the event action plan presented in **Appendix H** shall be carried out.

5. WASTE MANAGEMENT

5.1 Audit Requirements

5.1.1 The effective management of waste arising during the construction phase will be monitored through the site audit programme. Regular audits and site inspections should be carried out to ensure that the recommended good site practices and other mitigation measures are implemented by the Contractor.

5.1.2 The audit should look at all aspects of on-site waste management practices including the waste generation, storage, recycling, transport and disposal. The aims of waste audit are:

- to ensure the waste arising from the works are handled, stored, collected, transferred and disposed of in an environmentally acceptable manner;
- verify the implementation status and evaluate the effectiveness of the mitigation measures; and
- to encourage the reuse and recycling of material.

5.2 Results and Observations

5.2.1 C&D materials and wastes sorting were carried out on site. Receptacles were available for C&D wastes and general refuse collection.

5.2.2 The amount of wastes generated by the site activities in the reporting month is shown in **Appendix I**.

5.2.3 The Contractor is advised to properly maintain on site C&D materials and wastes collection, sorting and recording system and maximize reuse / recycle of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.

5.2.4 The Contractor is reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

6. SITE INSPECTION

6.1 Site Inspection

- 6.1.1 Site inspections were carried out weekly to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. A summary of the mitigation measures implementation schedule is provided in **Appendix J**.
- 6.1.2 In the reporting month, five site inspections were carried out on 2, 8, 15, 23 and 30 June 2016. Three of them, held on 2, 15 and 30 June 2016 were the joint inspections with the IEC, ER, the Contractor and the ET.
- 6.1.3 No outstanding issues were reported during the reporting month. Details of observations recorded during the site inspections are summarized in **Appendix M**.
- 6.1.4 All the follow-up actions requested by Contractor's ET and IEC during the site inspections were undertaken as reported by the Contractor and confirmed in the following weekly site inspection conducted during the reporting month.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars.

7. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

7.1 Environmental Exceedance

7.1.1 No Action / Limit Level exceedance was recorded for 24-hr TSP and construction noise at KTD1a, KTD2a and KER1a in the reporting month.

7.2 Complaints, Notification of Summons and Prosecution

7.2.1 No complaint, inspection notice, notification of summons or prosecution was received in this reporting month. Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix L**.

8. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

8.1 Implementation Status

8.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting month is summarized in **Appendix J**. Status of required submission under the EP during the reporting period is summarized in **Table 8.1**.

Table 8.1 Status of Required Submission under Environmental Permit

EP Condition	Submission	Submission Date
<u>EP-337/2009</u>		
Condition 2.3	Management Organization of Main Construction Companies	18/12/2015
Condition 2.4	Design Drawing of the Project	18/12/2015
Condition 2.11	Landscape Mitigation Plan(s)	18/12/2015
Condition 3.3	Monthly EM&A Report (May 2016)	14/6/2016
<u>EP-339/2009/A</u>		
Condition 2.4	Management Organization of Main Construction Companies	18/12/2015
Condition 2.5	Design Drawing of the Project	18/12/2015
Condition 3.3	Monthly EM&A Report (May 2016)	14/6/2016
<u>EP-451/2013</u>		
Condition 2.3	Management Organization of Main Construction Companies	18/12/2015
Condition 2.4	Design Drawing of the Project	18/12/2015
Condition 2.5	Landscape Mitigation Plan(s)	18/12/2015
Condition 2.10	Supplementary Contamination Assessment Report	18/12/2015
Condition 3.3	Baseline Monitoring Report	12/2/2016
Condition 3.4	Monthly EM&A Report (May 2016)	14/6/2016

9. FUTURE KEY ISSUES

9.1 Construction Programme for the Next Two Months

- Carrying out pre-drilling;
- Carrying out pumping test for Supporting Underground Structure (SUS);
- Implementation of Temporary Traffic Arrangement (TTA);
- Temporary diversion of existing Underground Utility (UU) at Zone 1 to Zone 4;
- Setting up temporary barging point;
- Erection of scaffolding and demolition of Radar Tower;
- Setting up stockpiling area at Portion I and K;
- Construction of subway B at Zone 1;
- Construction of H piles at Zone 1, 3 & 4;
- Construction of temporary road at Zone 2, 3 & 4;
- Construction of guide walls and D-walls at Zone 2 & 3; and
- Installation of bulkhead wall at Zone 1.

9.2 Key Issues for the Coming Month

- 9.2.1 Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality, waste management and landscape and visual impact.

9.3 Monitoring Schedules for the Next Three Months

- 9.3.1 The tentative schedules for environmental monitoring in the coming three months are provided in **Appendix E**.

10. CONCLUSIONS

- 10.1.1 24-hour TSP impact monitoring and construction noise monitoring were carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.
- 10.1.2 No complaint of air quality was received. Therefore, no impact 1-hour TSP monitoring was conducted in the reporting month.
- 10.1.3 Five no. of environmental site inspections were carried out in June 2016. Recommendations on mitigation measures on air quality, water quality, noise, waste management and landscape and visual impact were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 10.1.4 Five weekly Landscape and Visual Site audits were carried out on 2, 8, 15, 23 and 30 June 2016 and three of them, 2, 15 and 23 June 2016 were carried out by a Registered Landscape Architect in the reporting month. The weekly Landscape and Visual Impact reports were counter-signed by IEC as according to the requirement of EM&A Manual (AEIAR-130/2009).
- 10.1.5 Referring to the Contractor's information, no environmental complaint, notification of summons and successful prosecution was received in the reporting month.

10.2 Comment and Recommendations

- 10.2.1 The recommended environmental mitigation measures, as proposed in the EIA reports and EM&A Manuals shall be effectively implemented to minimize the potential environmental impacts from the Project. The EM&A programme would effectively monitor the environmental impacts generated from the construction activities and ensure the proper implementation of mitigation measures.
- 10.2.2 According to the environmental audit performed in the reporting month, the following recommendations were made:

Air Quality Impact

- Open stockpiles shall be covered by unobtrusive sheeting to prevent dust emission.
- Stock of more than 20 bags of cement or PFA should be covered entirely by impervious sheeting or placed in area sheltered on top and 3 sides.

Construction Noise Impact

- No specific observation was identified in the reporting month.

Water Quality Impact

- Implement effective/preventive measures to prevent accumulation of stagnant water.
- Surface runoff shall be prevented from entering the discharge channel directly. Sediment in the channel shall be cleaned up.

Chemical and Waste Management

- Chemical and Waste Management shall be provided properly.
- Construction waste shall be removed regularly.
- Chemicals and lubricant shall be stored on drip tray properly. The hole of drip tray shall be sealed to prevent leakage of chemicals
- Different types of waste shall be segregated and stored in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, sans-serif font. The text is white and is set against a black rectangular background that has a thin white border.

Landscape and Visual Impact

- Open stockpiles shall be covered by unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.

Permit / Licenses

- No specific observation was identified in the reporting month.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238


Fax : (852)-24508032

Email : mcl@fugro.com.hk



Figure 1

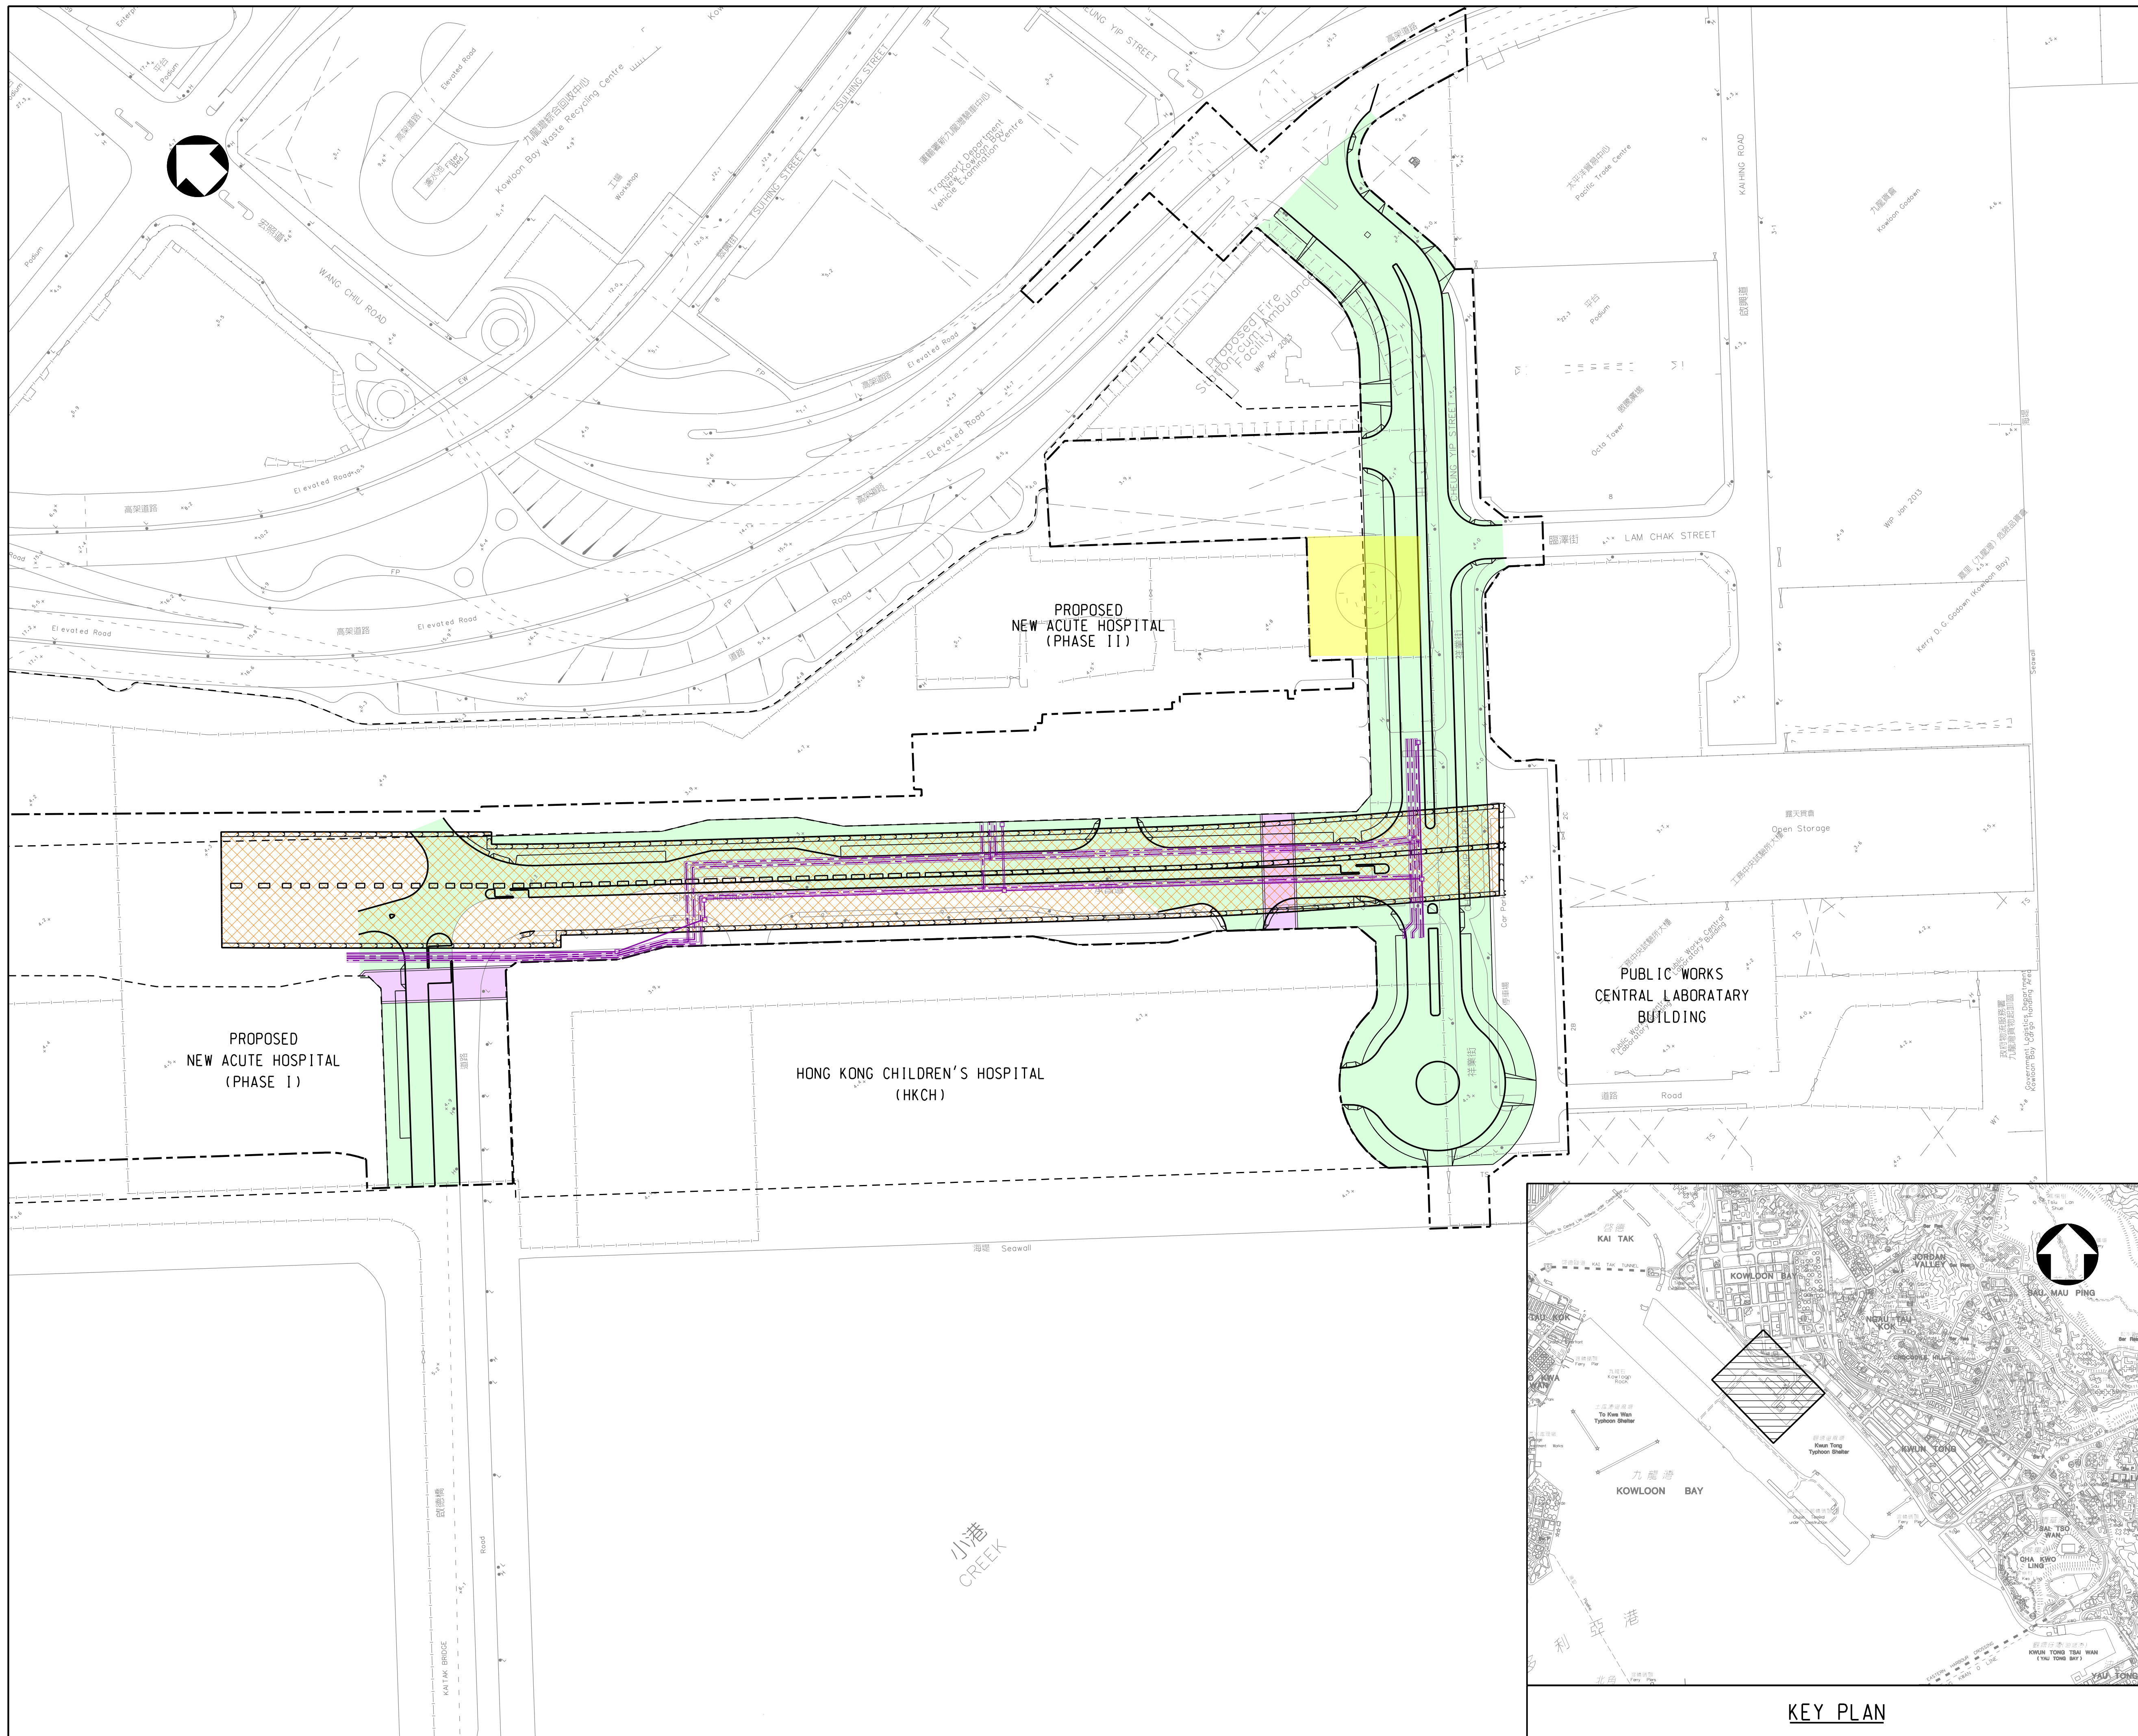Project General Layout



- LEGENDS:**
- SITE BOUNDARY
 - HOSPITAL SITE BOUNDARY
 - ▨ PROPOSED SUPPORTING UNDERGROUND STRUCTURE
 - ▨ PROPOSED SUBWAYS
 - ▨ PROPOSED ROADWORKS
 - ▨ PROPOSED DISTRICT COOLING SYSTEM
 - DEMOLITION OF RADAR TOWER

Rev.	Date	Drawn	Description	Checked	Approved




PROJECT
 CONTRACT NO. KL/2014/03
 KAI TAK DEVELOPMENT - STAGE 3
 INFRASTRUCTURE WORKS FOR
 DEVELOPMENTS AT THE SOUTHERN PART OF
 THE FORMER RUNWAY

TITLE
GENERAL LAYOUT PLAN

DESIGNED	ENG. CHECK
DRAWN	COORDINATION
DWG. CHECK	APPROVED
SCALE AT A1 1 : 1000	STATUS REV A

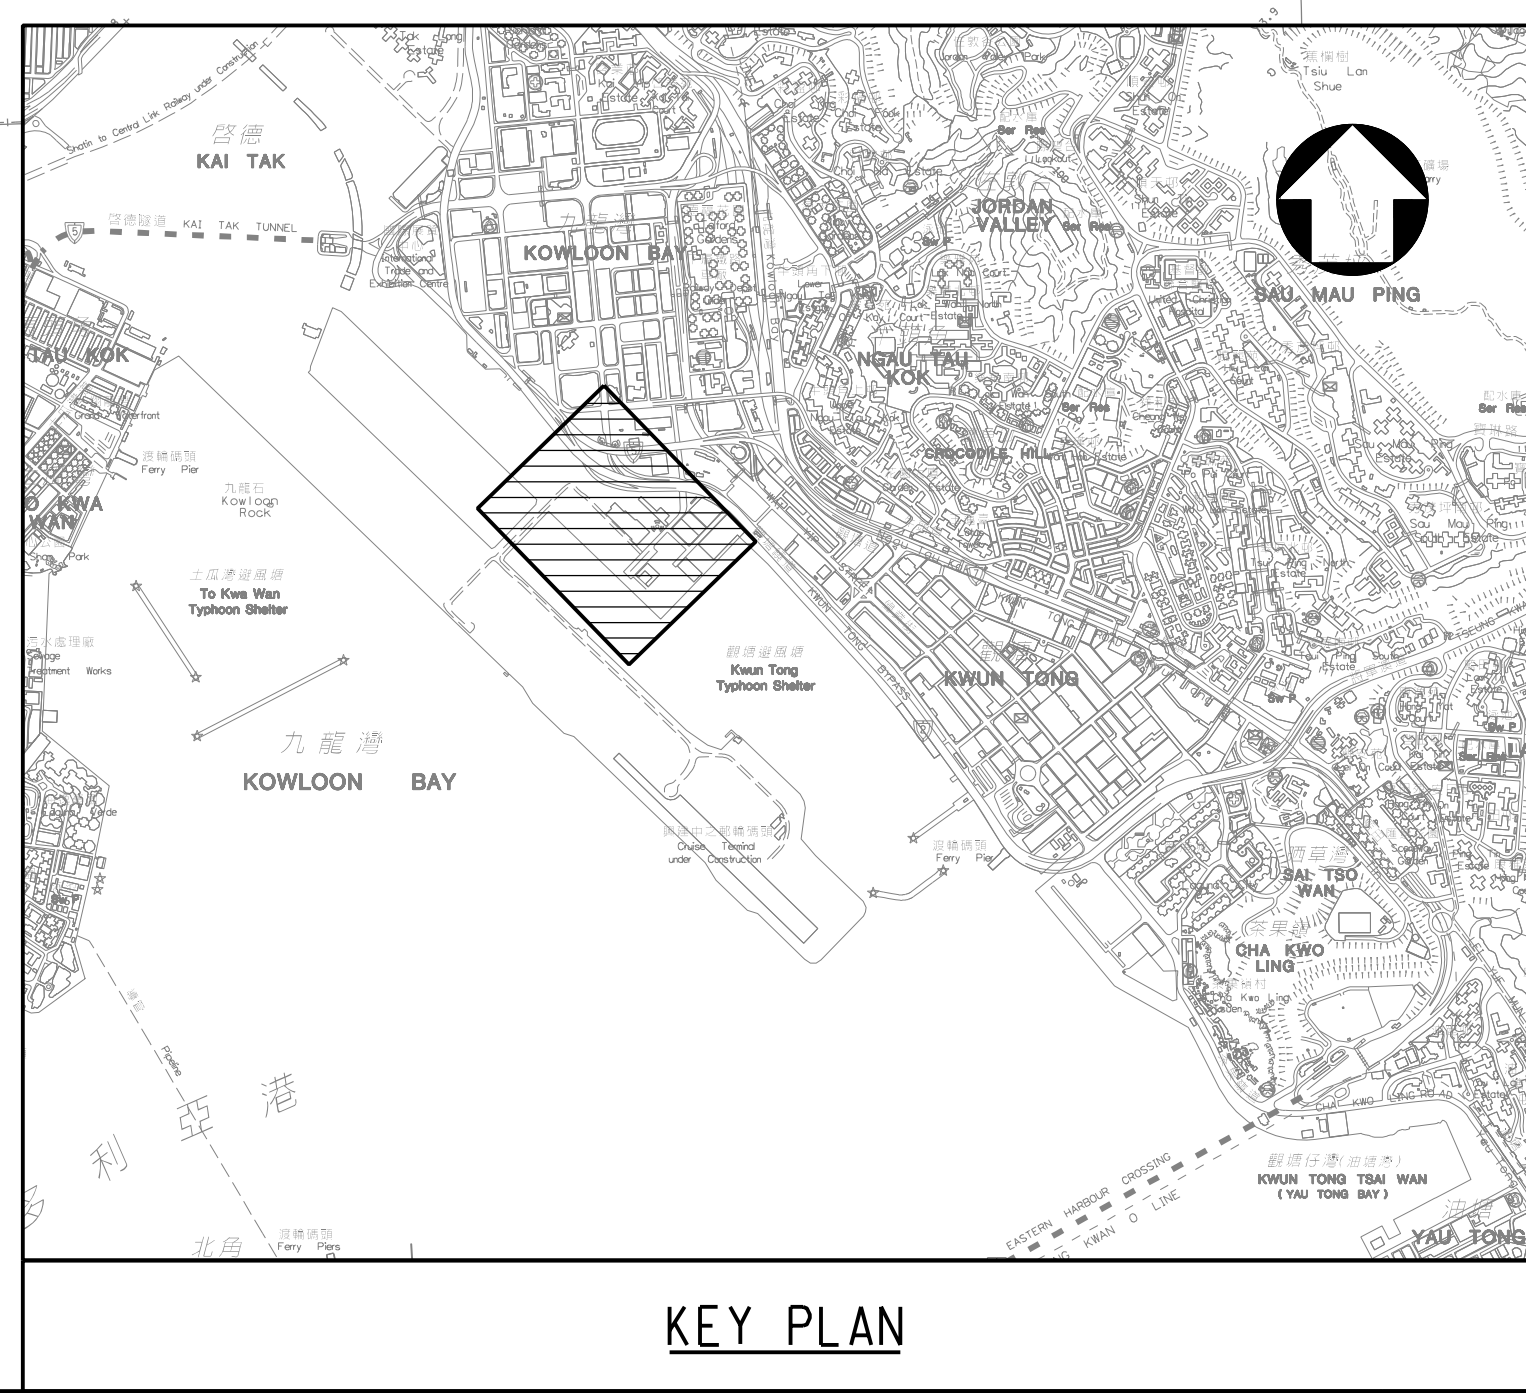Drawing No. **FIGURE 1.0**
 © Copyright reserved



KEY PLAN

PRINTED BY: kitchan 18/2/2015 13:00:43
 FILENAME: K:\91164 Trunk Road T2\Tender Drawing (Contract I)\Figure 1.dgn

MATERIALAB CONSULTANTS LIMITED

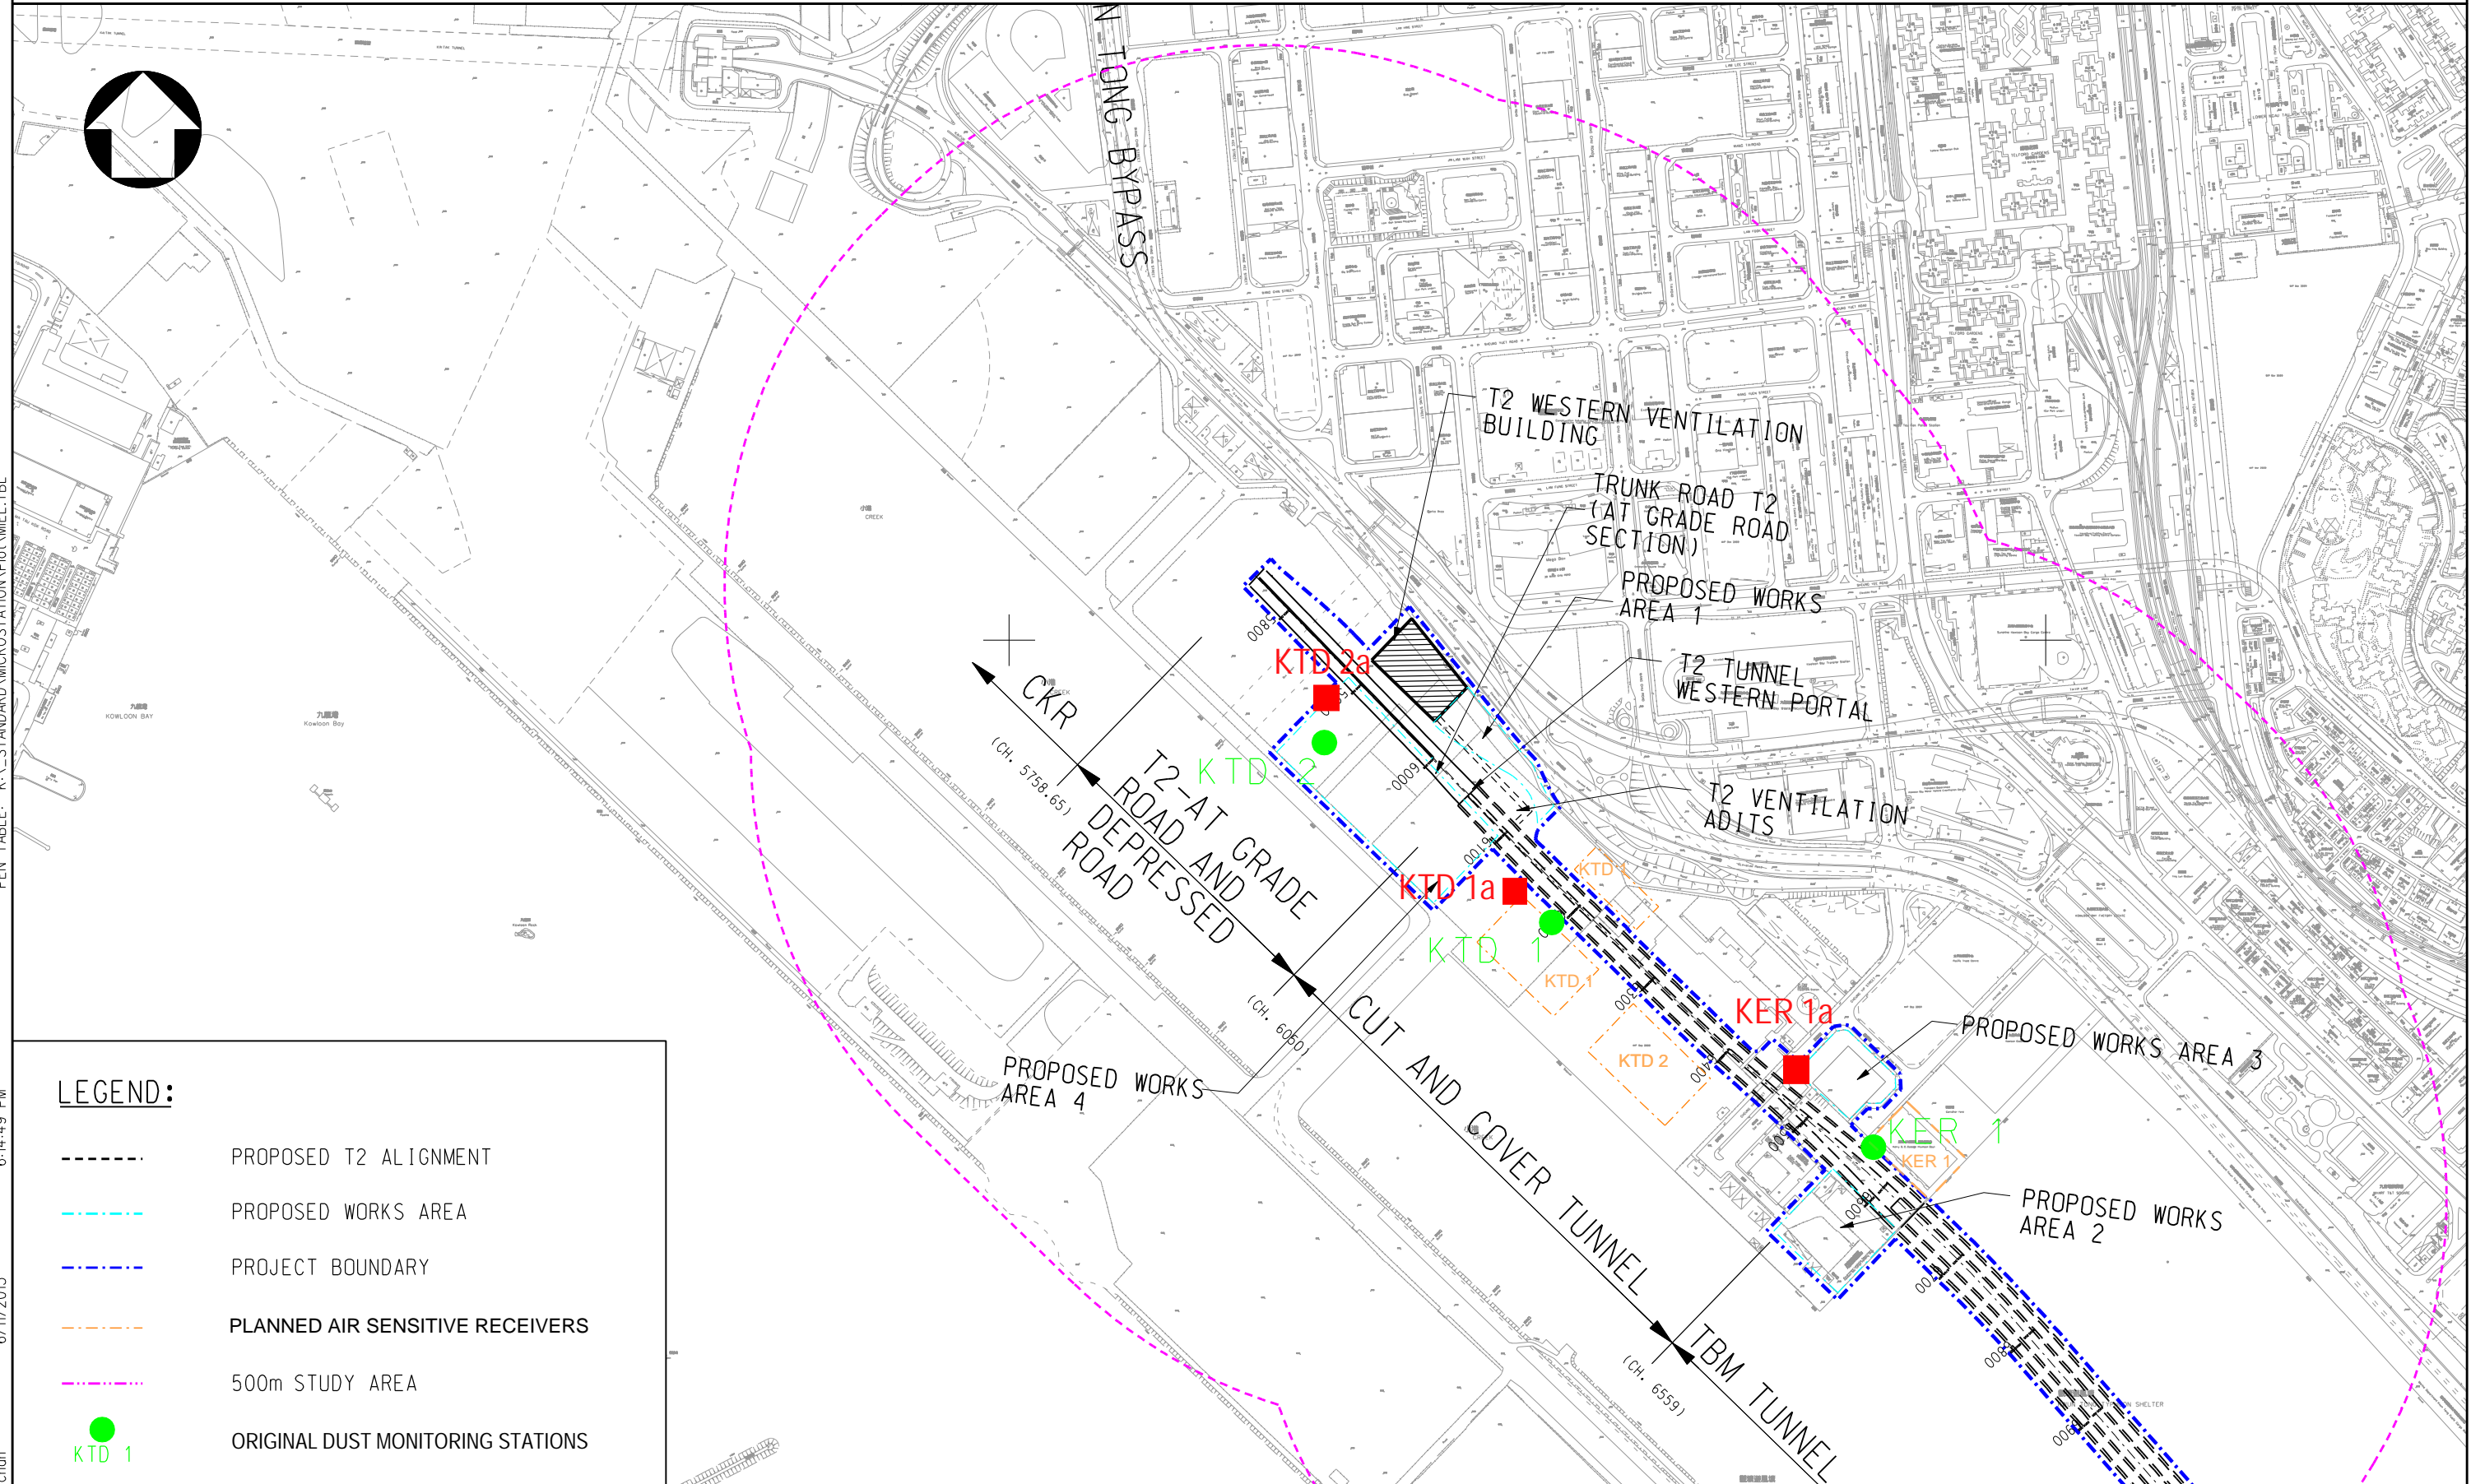
Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk










Figure 2

Air and Noise Monitoring Locations



LEGEND:

-  PROPOSED T2 ALIGNMENT
-  PROPOSED WORKS AREA
-  PROJECT BOUNDARY
-  PLANNED AIR SENSITIVE RECEIVERS
-  500m STUDY AREA
-  ORIGINAL DUST MONITORING STATIONS

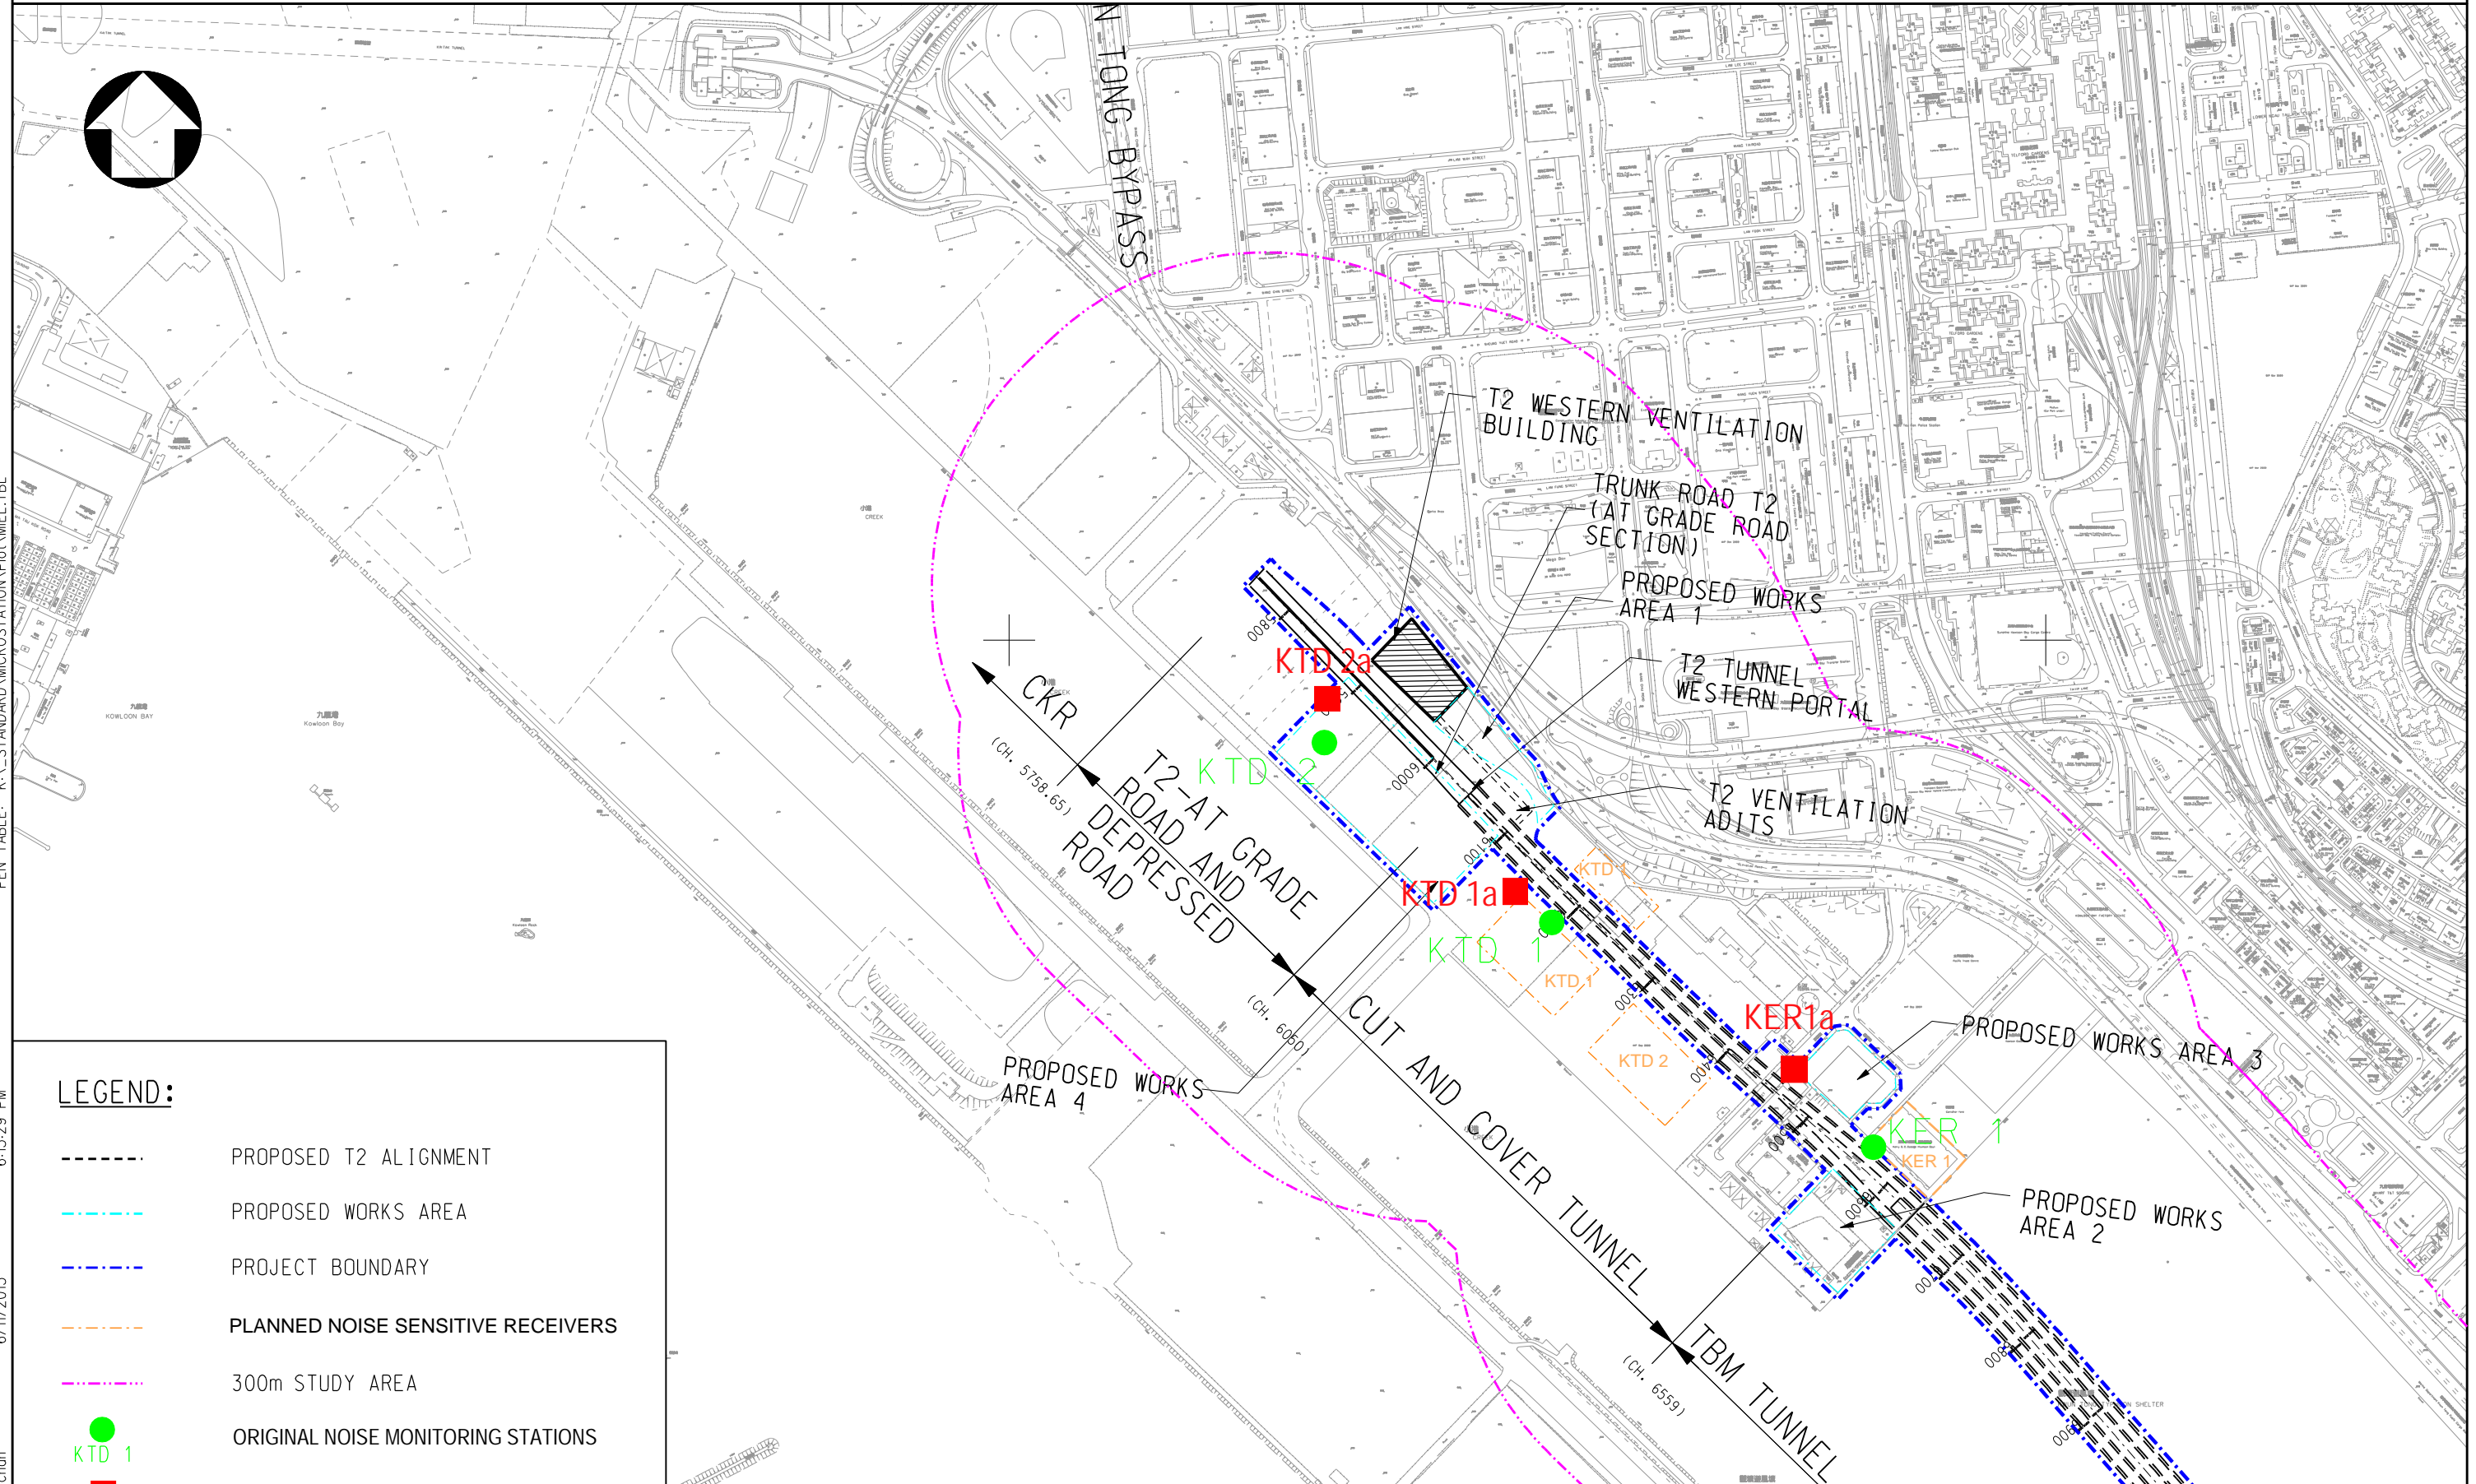
-  PROPOSED DUST MONITORING STATIONS

Drawing title








IDENTIFIED DUST MONITORING STATIONS AT SOUTH APRON OF FORMER KAI TAK AIRPORT

Original Size	A3	Scale	1 : 6000	Date	30/01/2012
© Copyright reserved		File name	Drawing No. FIGURE 2.1a(revised)		
Rev.	Description	Date	Rev. --		

PRINTER NAME: PDFCreator
 PLOT DRV: k:\91164 Trunk Road t2\Cad Admin\A3_colour.plt
 PRINTED BY: kitchen
 6/11/2013 6:14:49 PM



LEGEND:

-  PROPOSED T2 ALIGNMENT
-  PROPOSED WORKS AREA
-  PROJECT BOUNDARY
-  PLANNED NOISE SENSITIVE RECEIVERS
-  300m STUDY AREA
-  ORIGINAL NOISE MONITORING STATIONS
-  PROPOSED NOISE MONITORING STATIONS

PRINTER NAME: PDFCreator
 PLOT DRV: k:\91164 Trunk Road T2\Cad Admin\A3_colour.plt
 PRINTED BY: kitchen
 6/11/2013 6:15:29 PM

Drawing title

IDENTIFIED NOISE MONITORING STATIONS AT SOUTH APRON OF FORMER KAI TAK AIRPORT

Original Size

A3

Scale 1 : 6000

Date 30/01/2012

File name

© Copyright reserved

Drawing No.

FIGURE 3.1a (revised)

Rev.

--

Rev.	Description	Date

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

MaterialLab

Appendix A
Construction Programme

KL/2014/03 Kai Tak Development-Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors	2016				
							May	Jun	Jul	Aug	Sep
KL/2014/03-Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway											
Preliminaries, Alternative Design, Submission and Approval											
	Alternative Design for Supporting Underground Structure(SUS)	241	24-Nov-15 A	24-Aug-16							
K-PA-ADS-100	AIP Submission and approval	35	24-Dec-15 A	10-Jun-16	K-PA-ADS-090	K-PA-ADS-135, K-1A-SV1-008, K-1A-SV1-320					
K-PA-ADS-110	DDA Submission and approval- Tunnel box from CH6+150 to CH6+227	35	19-May-16 A	04-Jul-16	K-PA-ADS-100						
K-PA-ADS-115	DDA Submission and approval- SUS D-Wall from CH6+227 to CH6+568	35	26-Feb-16 A	24-Jun-16	K-PA-ADS-100	K-1A-SV3-135, K-1A-SV2-230,					
K-PA-ADS-135	DDA Submission and approval- SUS Top&Base slab and Intermediate wall from CH6+227 to CH6+568	35	20-Jul-16	24-Aug-16	K-PA-ADS-100	K-1A-SV2-420, K-1A-SUS-800,					
General Submission Under PS											
	Programming / Reporting	60	19-Mar-16 A	04-Jun-16							
	Works Programme	60	19-Mar-16 A	04-Jun-16							
K-PA-GSP-420	Prepare & submit Works Programme	60	19-Mar-16 A	04-Jun-16	K-PA-GSP-410	K-PA-GSP-430					
Major Temporary Works Design											
K-PA-GSP-6800	ELS design for construction of SUS and ventilation adit from CH6+150 to CH6+227 - vertical member	35	07-Jan-16 A	13-Jun-16	K-DW-PRE-120, K-PA-GSP-665, K-1A-SV1-320						
K-PA-GSP-6810	ELS design for construction of SUS and ventilation adit from CH6+150 to CH6+227 - horizontal member	35	06-May-16 A	20-Jun-16	K-PA-GSP-665, K-PA-GSP-665, K-1A-SV1-320						
K-PA-GSP-6820	ELS design for construction of SUS from CH6+467 to CH6+568 in Zone 2 to 4	35	19-Aug-16	22-Sep-16	K-PA-GSP-679, K-PA-GSP-679, K-1A-SV2-420, K-1A-SUS-720, K-PA-GSP-7460, K-4A-BAY-150						
K-PA-GSP-6840	ELS design for construction of subway A	35	19-Aug-16	22-Sep-16	K-PA-GSP-679, K-PA-GSP-679, K-1A-SV2-420, K-1A-SUS-720, K-PA-GSP-7460, K-4A-BAY-150						
K-PA-GSP-6870	Temporary vehicular and pedestrian access for HKCH	35	10-Jul-16	13-Aug-16	K-PA-GSP-679, K-PA-GSP-679, K-1A-SV2-420, K-1A-SUS-720, K-PA-GSP-7460, K-4A-BAY-150						
K-PA-GSP-7000	ELS design for construction of DCS	35	20-Jul-16	23-Aug-16	K-PA-GSP-679, K-PA-GSP-679, K-1A-SV2-420, K-1A-SUS-720, K-PA-GSP-7460, K-4A-BAY-150						
K-PA-GSP-8350	Temporary work design for construction of subway structure	35	20-Jun-16	24-Jul-16	K-PA-GSP-679, K-PA-GSP-679, K-1A-SV2-420, K-1A-SUS-720, K-PA-GSP-7460, K-4A-BAY-150						
K-PA-GSP-8750	Pumping Test for SUS Cofferdam in Zone 1	35	09-Mar-16 A	31-May-16	K-PA-GSP-6850	K-PA-GSP-8850					
K-PA-GSP-8850	Pumping Test for SUS Cofferdam in Zone 2 to 4	35	25-Jul-16	28-Aug-16	K-PA-GSP-8750	K-1A-SUS-700, K-PA-GSP-6860,					
Major Construction Works Method Statement											
K-PA-GSP-7145	Method statement of Excavation and ELS - Engineer's comment and approval	28	19-May-16 A	22-Jun-16	K-PA-GSP-7140	K-1A-SV1-320, K-1A-SV2-420					
K-PA-GSP-7325	Method statement for Demolition of Rader Tower - Engineer's comment and approval	28	09-May-16 A	08-Jun-16	K-PA-GSP-7320	K-02-DRT-1050, K-PA-GSP-7340, K-02-DCH-135, K-02-DCH-130					
K-PA-GSP-7345	Method statement for Demolition of Guard House - Engineer's comment and approval	28	09-May-16 A	08-Jun-16	K-PA-GSP-7340	K-02-DCH-135, K-02-DCH-130					
K-PA-GSP-7400	Method statement for Construction of tunnel box structure	28	20-Jun-16	17-Jul-16	K-PA-GSP-7400	K-PA-GSP-7405					
K-PA-GSP-7405	Method statement for Construction of tunnel box structure - Engineer's comment and approval	28	18-Jul-16	14-Aug-16	K-PA-GSP-7400	K-1A-SV1-350					
K-PA-GSP-7485	Method statement for Construction of subway B - Engineer's comment and approval	28	31-May-16 A	27-Jun-16	K-PA-GSP-7480	K-4B-BAY-2000					
Temporary Utility Diversion/ Relocation											
K-PA-GSP-666	Submission and approval utility diversion scheme in Zone 1	30	12-Jan-16 A	02-Jun-16	K-PA-GSP-666	K-PA-GSP-668, K-PA-TUD-1000, K-PA-GSP-845					
K-PA-GSP-667	Submission and approval utility diversion scheme in Zone 2,3&4	45	25-Jan-16 A	08-Jun-16	K-PA-GSP-665						
Temporary Utility Diversion Works at Zone 1											
K-PA-TUD-0500	Procurement and delivery watermain material	45	07-May-16 A	30-Jun-16	K-PA-GSP-666	K-PA-TUD-1100, K-PA-TUD-2000, K-PA-TUD-1120, K-PA-TUD-1400					
K-PA-TUD-1100	Excavation trench for DN600 MS and DI fresh watermain	30	14-Jun-16	19-Jul-16	K-PA-TUD-0500	K-PA-TUD-1100, K-PA-TUD-1400					
K-PA-TUD-1120	Laying DN600 MS and DI fresh watermain at subway B & Zone 1	25	02-Jul-16	30-Jul-16	K-PA-TUD-1100	K-PA-TUD-1150					
K-PA-TUD-1150	DN600 DI connected (X1 and X2)	0		29-Aug-16	K-PA-TUD-1120	K-PA-TUD-1160					
K-PA-TUD-1160	DN600 DI connected (X3)	0		29-Aug-16	K-PA-TUD-1150	K-PA-TUD-1250					
K-PA-TUD-1200	Excavation trench for DN300 MS salt watermain at subway B & Zone 1	30	14-Jun-16	19-Jul-16	K-PA-TUD-0500	K-PA-TUD-1210, K-PA-TUD-2600					
K-PA-TUD-1210	Laying DN600 MS and DI fresh watermain at subway B & Zone 1	25	02-Jul-16	30-Jul-16	K-PA-TUD-1200	K-PA-TUD-1250					
K-PA-TUD-1250	DN300 DI connected (Y1 and Y2)	0		29-Aug-16	K-PA-TUD-1160, K-PA-TUD-1210						
K-PA-TUD-1400	Excavation trench for 600UC, 900 and 450 MS pipe and manhole at Zone 1	15	03-May-16 A	18-Jun-16	K-PA-TUD-1100	K-PA-TUD-1500, K-PA-TUD-1410, K-PA-TUD-1420					
K-PA-TUD-1410	Construction 600UC at Zone 1	10	16-May-16 A	22-Jun-16	K-PA-TUD-1400						
K-PA-TUD-1420	Laying 900 and 450 MS pipe at Zone 1	15	16-May-16 A	29-Jun-16	K-PA-TUD-1410	K-PA-TUD-1450					

█ Remaining Level of Effort █ Remaining Work
█ Actual Work █ Critical Remaining Work

3 MRP - June to August (based on IWP Rev.2)

Date	Revision	Checked	Approved
31-May-16	2		

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors	2016									
							May	Jun	Jul	Aug	Sep					
K-IA-SV1-340	Installation of socketted H-piles for Eastbound and Westbound	70	22-Apr-16 A	25-Jun-16	K-PA-GSP-713, K-IA-SV1-120, K-IA-SV1-340, K-IA-SV1-140	K-IA-SV2-300, K-IA-SV3-150, K-IA-SV1-220										
K-IA-SV1-462	Loading test for socketted H-Piles	8	29-Jun-16	09-Jul-16												
Tunnel Box Structure																
K-IA-SV1-200	Installation of dewatering well, observation well and recharging well in Zone 1	30	25-Jun-16	30-Jul-16	K-IA-SV1-140, K-IA-SV1-340, K-IA-SV1-200	K-IA-SV1-210										
K-IA-SV1-210	Pumping test for excavation in Zone 1	14	01-Aug-16	16-Aug-16												
K-IA-SV1-220	Excavation and ELS up to formation level of tunnel box(6+191-6+224)	30	17-Aug-16	21-Sep-16	K-IA-SV1-008, K-IA-SV1-462	K-IA-SV1-230, K-IA-SV1-320										
SUS and Ventilation Adits from CH6+224 to CH6+348 in Zone 2																
D-Wall and Piling Works																
E/B D-Wall and Socketted H-Piles(CH6+224 to CH6+348) in TTA Stage 1																
K-IA-SV2-125	Construction of guide wall	25	25-Apr-16 A	08-Jun-16	K-PA-GSP-712, K-IA-SV2-110	K-IA-SV2-130										
K-IA-SV2-127	Procurement and delivery H-pile material	60	01-Apr-16 A	02-Jun-16		K-IA-SV3-280, K-IA-SV3-150, K-IA-SV2-130										
K-IA-SV2-128	Plant mobilization and set up for D-wall and socketted H-Pile	5	08-Jun-16	15-Jun-16	K-IA-SV1-130, K-PA-GSP-712, K-IA-SV2-128	K-IA-SV2-230, K-IA-SV2-790, K-IA-SV2-800, K-IA-SV2-205										
K-IA-SV2-130	Construction of D-wall eastbound(CH6+254 to CH6+348)	72	24-Jun-16	19-Sep-16												
K-IA-SV2-300	Installation of socketted H-piles (CH6+227 to CH6+348)	112	13-Jul-16	23-Nov-16	K-IA-SV1-340, K-IA-SV1-140											
W/B D-Wall (CH6+224 to CH6+348) in TTA Stage 2																
K-IA-SV2-210	Predrilling works	42	02-Aug-16	20-Sep-16	K-IA-UDN-120	K-IA-SV3-252, K-IA-SV2-215										
SUS Structure from CH6+348 to 6+467 in Zone 3																
D-Wall and Piling Works																
E/B D-Wall and Socketted H-Piles in TTA Stage 1																
K-IA-SV3-132	Construction of guide wall	21	31-May-16	24-Jun-16	K-IA-SV3-130	K-IA-SV3-136										
K-IA-SV3-133	Plant mobilization and set up for D-wall and socketted H-Pile	5	11-Jun-16	17-Jun-16	K-IA-SV1-120, K-PA-GSP-679	K-IA-SV3-136, K-IA-SV3-150										
K-IA-SV3-136	Construction of D-wall eastbound(CH6+348 to CH6+467)	62	25-Jun-16	06-Sep-16	K-IA-SV3-133, K-IA-SV3-132, K-IA-SV1-140, K-IA-SV1-340	K-IA-SV3-390, K-IA-SV3-490, K-IA-SV3-276										
K-IA-SV3-150	Installation of socketted H-piles (CH6+348 to CH6+467)	112	29-Jun-16	11-Nov-16												
W/B D-Wall in TTA Stage 1A																
K-IA-SV3-252	Predrilling works	32	02-Aug-16	07-Sep-16	K-IA-SV2-210	K-IA-SV3-480, K-IA-SV3-300, K-IA-SV3-321, K-IA-SV3-340										
K-IA-SV3-320	Construction of temporary diversion road for TTA stage 1A	94	31-May-16	20-Sep-16												
K-IA-SV3-321	Construction of temporary drainage at zone 2 to 4	25	31-May-16	29-Jun-16	K-IA-SV3-320	K-IA-SV3-322										
K-IA-SV3-322	Construction of concrete pavement at zone 4	14	13-Jun-16	28-Jun-16	K-IA-SV3-321	K-IA-SV3-323										
K-IA-SV3-323	Construction of concrete pavement at zone 3	14	29-Jun-16	15-Jul-16	K-IA-SV3-322	K-IA-SV3-324										
K-IA-SV3-324	Construction of concrete pavement at zone 2	25	16-Jul-16	13-Aug-16	K-IA-SV3-323	K-IA-SV3-325										
K-IA-SV3-325	Installation of street lighting	14	15-Aug-16	30-Aug-16	K-IA-SV3-324	K-IA-SV3-326										
SUS Structure from CH6+467 to 6+568 in Zone 4																
D-Wall and Piling Works																
E/B D-Wall and Socketted H-Piles in TTA Stage 1																
K-IA-SV3-100	Predrilling works	35	18-Jan-16 A	07-Jun-16	K-PK-SPD-200, K-PA-GSP-665, K-IA-SV3-100	K-IA-SV3-120, K-IA-SV3-130, K-IA-SV3-135, K-IA-SV3-120										
K-IA-SV3-110	Plant mobilization and set up for D-wall and socketted H-Pile	10	08-Jun-16	20-Jun-16												
K-IA-SV3-120	Construction of guide wall	21	08-Jun-16	04-Jul-16	K-IA-SV3-100, K-PA-GSP-712	K-IA-SV3-135										
K-IA-SV3-135	Construction of D-wall eastbound(CH6+467 to CH6+550)	91	05-Jul-16	21-Oct-16	K-PA-ADS-115, K-IA-SV3-110, K-IA-SV3-135, K-IA-SV2-127	K-IA-SV3-250, K-IA-SV3-152, K-IA-SV3-286										
K-IA-SV3-152	Installation of socketted H-piles(CH6+467 to CH6+550)	112	05-Jul-16	15-Nov-16												
W/B D-Wall, E/B D-Wall and End Wall in TTA Stage 1A																
K-IA-SV3-210	Predrilling works	32	02-Aug-16	07-Sep-16	K-IA-SV3-252	K-IA-SV3-220										
K-IA-SV3-220	Construction of guide wall	35	15-Aug-16	24-Sep-16	K-IA-SV3-210	K-IA-SV3-250										
Section 2 of the Works-Demolition of Radar Tower and Guard House																
K-02-DRG-110	Condition survey and installation of monitoring point	30	31-May-16	06-Jul-16	K-PK-SPD-230	K-02-DRT-1200, K-02-DRT-1050										
Demolition of Radar Tower																

█ Remaining Level of Effort █ Remaining Work
█ Actual Work █ Critical Remaining Work

3 MRP - June to August (based on IWP Rev.2)

Date	Revision	Checked	Approved
31-May-16	2		

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors	2016				
							May	Jun	Jul	Aug	Sep
K-02-DRT-1100	Demolition and erection of hoarding	40	16-May-16 A	18-Jun-16			Demolition and erection of hoarding				
K-02-DRT-1200	Erection of temporary scaffolding/proping	50	16-May-16 A	06-Jul-16	K-02-DRG-110, K-PA-GSP-7325	K-02-DRT-1300, K-02-DRT-1250,	Erection of temporary scaffolding/proping				
K-02-DRT-1250	Removal of asbestos materials	15	07-Jul-16	23-Jul-16	K-02-DRT-1200, K-02-DRT-1050		Removal of asbestos materials				
K-02-DRT-1270	Demolition G/F pump room	14	31-May-16 A	14-Jun-16	K-02-DRT-1200	K-02-DRT-1300	Demolition G/F pump room				
K-02-DRT-1300	Demolition and Removal of 13/F to Roof	40	07-Jul-16	22-Aug-16	K-PA-GSP-6940, K-02-DRT-1200, K-02-DRT-1300	K-02-DRT-1350, K-PK-SCC-204	Demolition and Removal of 13/F to Roof				
K-02-DRT-1350	Demolition and Removal of 11/F to 13/F	40	23-Aug-16	11-Oct-16	K-02-DRT-1300	K-02-DRT-1400	Demolition and Removal of 11/F to 13/F				
Demolition of Guard House		32	10-May-16 A	13-Jun-16			Demolition of Guard House				
K-02-DGH-140	Demolition of Guard House	32	10-May-16 A	13-Jun-16	K-02-DGH-130, K-02-DGH-135	K-PK-SCC-204	Demolition of Guard House				
Section 3 of the Works- Construction of District Cooling System (Subject to Excision)		90	24-Aug-16	09-Dec-16			Section 3 of the Works- Construction of District Cooling System (Subject to Excision)				
Preparation Works		90	24-Aug-16	09-Dec-16			Preparation Works				
K-03-DCS-095	Procurement and delivery of DCS pipe	90	24-Aug-16	09-Dec-16	K-PA-GSP-7300, K-PA-GSP-7000,	K-03-DCS-110	Procurement and delivery of DCS pipe				
Section 4B of the Works- Construction of Subway B (Subject to Excision)		73	27-May-16 A	10-Sep-16			Section 4B of the Works- Construction of Subway B (Subject to Excision)				
Bay 1&2		73	27-May-16 A	10-Sep-16			Bay 1&2				
K-4B-BAY-2000	Installation of sheetpile for Bay 1&2	15	27-May-16 A	17-Jun-16	K-PA-GSP-7485, K-PA-GSP-6850,	K-4B-BAY-2050, K-4B-BAY-220	Installation of sheetpile for Bay 1&2				
K-4B-BAY-2050	Excavation and ELS works of Bay 1&2	28	17-Jun-16	21-Jul-16	K-4B-BAY-2000		Excavation and ELS works of Bay 1&2				
K-4B-BAY-220	Construction of Bay 1	21	25-Jul-16	17-Aug-16	K-4B-BAY-2050, K-4B-BAY-2000,	K-4B-BAY-230	Construction of Bay 1				
K-4B-BAY-230	Construction of Bay 2	21	18-Aug-16	10-Sep-16	K-4B-BAY-220	K-4B-BAY-310, K-4B-BAY-235	Construction of Bay 2				
Section 7 of the Works-Preservation and Protection of Existing Trees		1200	29-Feb-16 A	12-Jun-19			Section 7 of the Works-Preservation and Protection of Existing Trees				
K-07-001-001	Section 7 of the Works-Preservation and Protection of Existing Trees	1200	29-Feb-16 A	12-Jun-19	K-DR-PRE-173, K-DR-PRE-175	K-PK-SCC-250	Section 7 of the Works-Preservation and Protection of Existing Trees				

█ Remaining Level of Effort █ Remaining Work
█ Actual Work █ Critical Remaining Work

3 MRP - June to August (based on IWP Rev.2)

Date	Revision	Checked	Approved
31-May-16	2		

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk




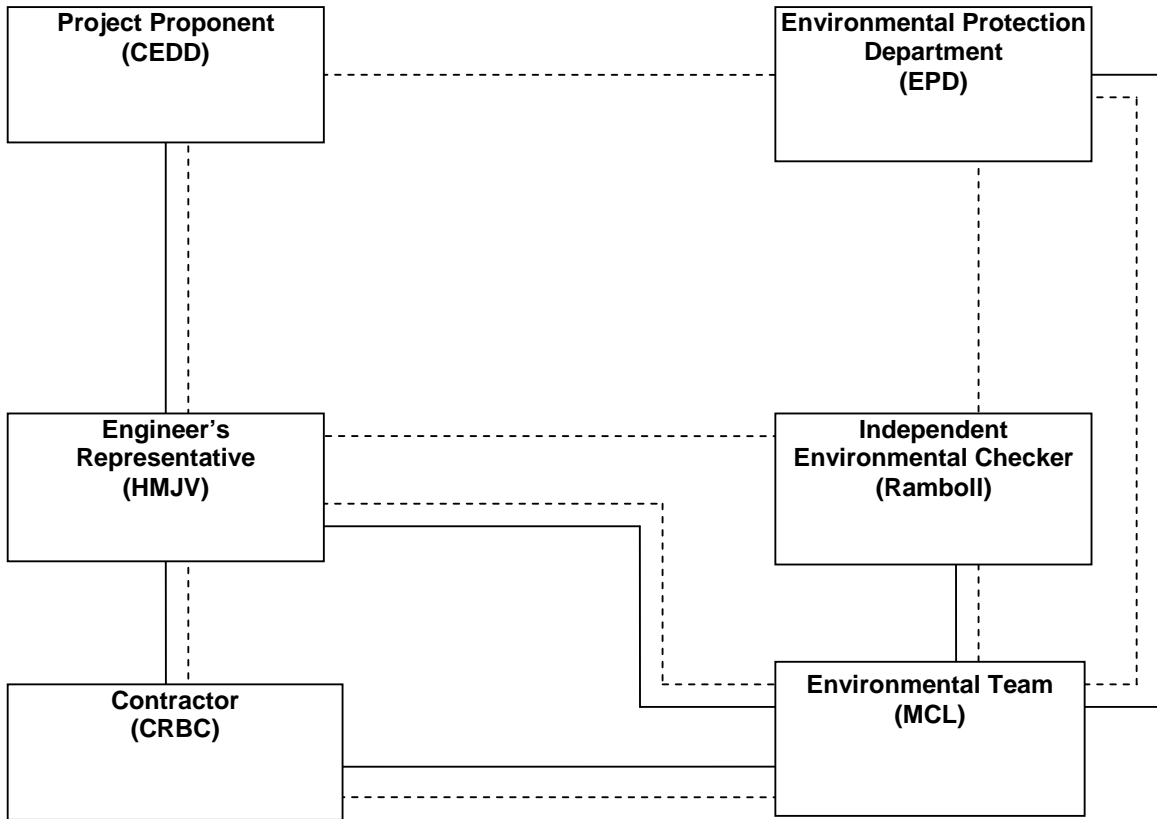
Appendix B

Project Organization Chart

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk



MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk



Appendix C

Action and Limit Levels for Air Quality and Noise

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

MaterialLab**Action and Limit Levels for 24-hr TSP and 1-hr TSP**

Parameter	Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
24-hr TSP ($\mu\text{g}/\text{m}^3$)	KTD1a	177	260
	KTD2a	157	
	KER1a	172	
*1-hr TSP ($\mu\text{g}/\text{m}^3$)	KTD1a	285	500
	KTD2a	279	
	KER1a	295	

Note:

1-hr TSP monitoring should be required in case of complaints.

Action and Limit Levels for Construction Noise, Leq (30min), dB(A)

Time Period	Location	Action	Limit
0700-1900 hrs on normal weekdays	KTD1a KTD2a KER1a	When one documented complaint is received	75 dB(A)

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars, one above and one below the text.

Appendix D

Calibration Certificates of Monitoring Equipment



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELS, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jan 14, 2016 Rootsmeter S/N 0438320 Ta (K) - 292
 Operator Tisch Orifice I.D. - 2456 Pa (mm) - 748.03

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER	ORFICE
					DIFF Hg (mm)	DIFF H2O (in.)
1	NA	NA	1.00	1.4420	3.2	2.00
2	NA	NA	1.00	1.0220	6.4	4.00
3	NA	NA	1.00	0.9130	7.9	5.00
4	NA	NA	1.00	0.8670	8.8	5.50
5	NA	NA	1.00	0.7170	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0002	0.6936	1.4174	0.9957	0.6905	0.8836
0.9959	0.9745	2.0045	0.9915	0.9701	1.2496
0.9938	1.0885	2.2411	0.9893	1.0836	1.3971
0.9926	1.1449	2.3504	0.9882	1.1398	1.4653
0.9874	1.3771	2.8347	0.9830	1.3710	1.7672
Qstd slope (m) = 2.07173			Qa slope (m) = 1.29728		
intercept (b) = -0.01761			intercept (b) = -0.01098		
coefficient (r) = 0.99996			coefficient (r) = 0.99996		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol} [(Pa - \text{Diff. Hg}) / 760] (298 / Ta)$$

$$Qstd = Vstd / \text{Time}$$

$$Va = \text{Diff Vol} [(Pa - \text{Diff Hg}) / Pa]$$

$$Qa = Va / \text{Time}$$

For subsequent flow rate calculations:

$$Qstd = 1/m \{ [\text{SQRT}(H2O(Pa/760) (298/Ta))] - b \}$$

$$Qa = 1/m \{ [\text{SQRT} H2O(Ta/Pa)] - b \}$$

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong.

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk



TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Project : Environmental Monitoring Works For Contract No. KLN/2015/07		Date of Calibration: 18-Apr-16
Location : KTD1a		Next Calibration Date: 17-Jul-16
Brand: Tisch	Technician: Jimmy Lui	
Model: TE-5170	S/N: 3478	

CONDITIONS			
Sea Level Pressure (hPa):	1001.4	Corrected Pressure (mm Hg):	761
Temperature (°C):	23	Temperature (K):	297

CALIBRATION ORIFICE			
Make: Tisch	Qstd Slope:	2.07173	
Model: TE-5025A	Qstd Intercept:	-0.01761	
Calibration Date: 14-Jan-16	Expiry Date:	14-Jan-17	
S/N: 2456			

CALIBRATIONS							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)	LINEAR REGRESSION
18	7.50	-4.80	12.300	1.705	64.00	64.15	Slope = 32.1712 Intercept = 9.1954 Corr. coeff.: 0.9995
13	6.40	-3.50	9.900	1.531	58.00	58.14	
10	5.10	-2.40	7.500	1.333	52.00	52.12	
7	3.80	-1.00	4.800	1.068	44.00	44.10	
5	2.90	-0.10	3.000	0.846	36.00	36.08	

Calculations:

$Qstd = 1/m[\sqrt{H2O(Pa/Pstd)(Tstd/Ta)}]-b]$

$IC = I[\sqrt{Pa/Pstd}(Tstd/Ta)]$

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pa = actual pressure during calibration (mm Hg)

Tstd = 298 deg K

Pstd = 760 mm Hg

For subsequent calculation of sampler flow:

$1/m((I)[\sqrt{298/Tav}(Pav/760)]-b)$

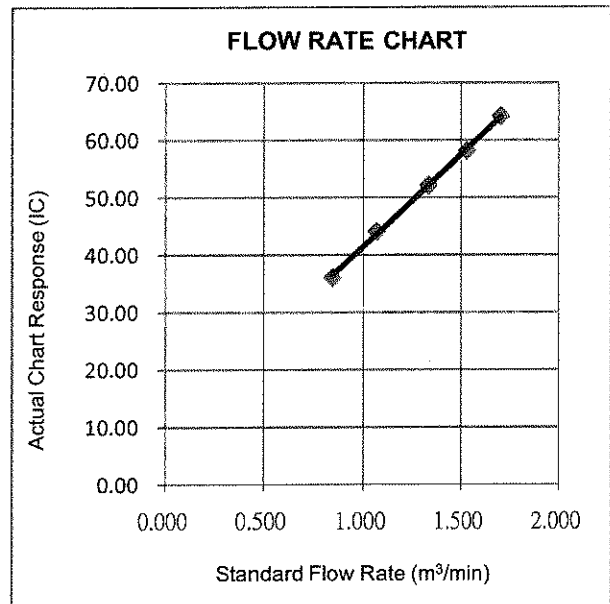
m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure



CHOI KAM HO
 Project Consultant

Report Date: 18th April, 2016

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong.

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk



TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Project : Environmental Monitoring Works For Contract No. KLN/2015/07		Date of Calibration: 18-Apr-16
Location : KTD2a		Next Calibration Date: 17-Jul-16
Brand: Tisch	Technician: Jimmy Lui	
Model: TE-5170	S/N: 3838	

CONDITIONS			
Sea Level Pressure (hPa):	1001.4	Corrected Pressure (mm Hg):	761
Temperature (°C):	23	Temperature (K):	297

CALIBRATION ORIFICE			
Make: Tisch	Qstd Slope:	2.07173	
Model: TE-5025A	Qstd Intercept:	-0.01761	
Calibration Date: 14-Jan-16	Expiry Date:	14-Jan-17	
S/N: 2456			


CALIBRATIONS							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)	LINEAR REGRESSION
18	7.20	-4.60	11.800	1.670	51.00	51.12	Slope = 28.4227
13	6.00	-3.40	9.400	1.492	44.00	44.10	Intercept = 2.7436
10	4.90	-2.30	7.200	1.307	40.00	40.09	Corr. coeff.: 0.9960
7	3.70	-1.00	4.700	1.057	32.00	32.07	
5	2.80	-0.10	2.900	0.832	27.00	27.06	

Calculations:

Qstd = 1/m[√(H2O(Pa/Pstd)(Tstd/Ta))-b]
 IC = I[√(Pa/Pstd)(Tstd/Ta)]
 Qstd = standard flow rate
 IC = corrected chart response
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pa = actual pressure during calibration (mm Hg)
 Tstd = 298 deg K
 Pstd = 760 mm Hg

For subsequent calculation of sampler flow:

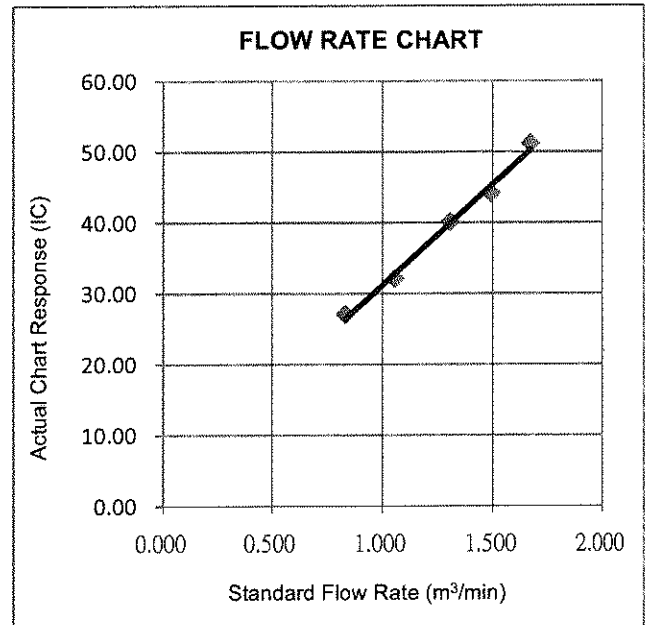1/m((I)[√(298/Tav)(Pav/760)]-b)
 m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure



CHOI KAM HO
 Project Consultant

Report Date: 18th April, 2016

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong.

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk



TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Project : Environmental Monitoring Works For Contract No. KLN/2015/07			Date of Calibration: 18-Apr-16		
Location : KER1a			Next Calibration Date: 17-Jul-16		
Brand:	Tisch			Technician: Jimmy Lui	
Model:	TE-5170	S/N:	3482		


CONDITIONS					
Sea Level Pressure (hPa):	1001.4	Corrected Pressure (mm Hg):	761		
Temperature (°C):	23	Temperature (K):	297		

CALIBRATION ORIFICE					
Make:	Tisch	Qstd Slope:	2.07173		
Model:	TE-5025A	Qstd Intercept:	-0.01761		
Calibration Date:	14-Jan-16	Expiry Date:	14-Jan-17		
S/N:	2456				

CALIBRATIONS							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m ³ /min)	I (chart)	IC (corrected)	LINEAR REGRESSION
18	12.00	2.00	10.000	1.538	60.00	60.14	Slope = 38.0025
13	11.40	2.30	9.100	1.468	58.00	58.14	Intercept = 1.6770
10	10.50	3.50	7.000	1.289	50.00	50.12	Corr. coeff. 0.9979
7	9.00	4.50	4.500	1.035	40.00	40.09	
5	8.20	5.30	2.900	0.832	34.00	34.08	

Calculations:

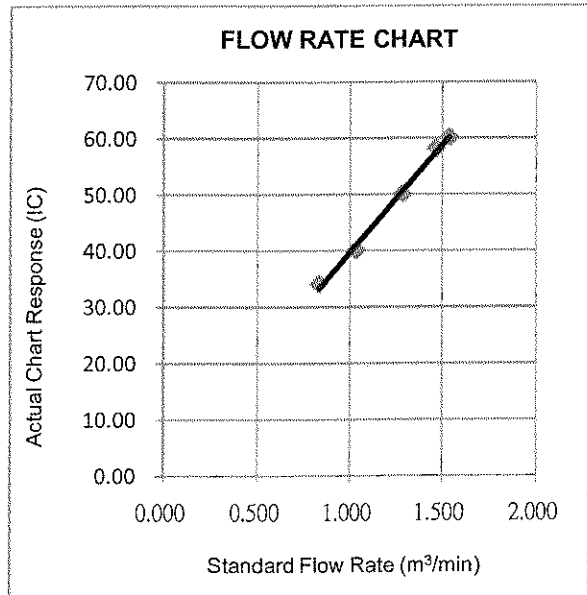$Qstd = 1/m[\sqrt{(H2O(Pa/Pstd)(Tstd/Ta))}] - b$
 $IC = I[\sqrt{(Pa/Pstd)(Tstd/Ta)}]$
 Qstd = standard flow rate
 IC = corrected chart response
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pa = actual pressure during calibration (mm Hg)
 Tstd = 298 deg K
 Pstd = 760 mm Hg
For subsequent calculation of sampler flow:
 $1/m((I)[\sqrt{(298/Tav)(Pav/760)}] - b)$
 m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure



AS

CHOI KAM HO
Project Consultant

Report Date: 18th April, 2016

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report no.: 940891CA160442(1)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
Manufacturer : Casella (Model no. CEL-120/1)
Serial No. : 5230742
Next Calibration Date : 02-Mar-2017
Specification Limit : ± 0.5 dB

Laboratory Information


Description : Reference Sound Level Meter
Equipment ID. : R-119-1
Date of Calibration : 03-Mar-2016 Ambient Temperature : 21 °C
Calibration Location : Calibration Laboratory of Materialab
Method Used : By direct comparison

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	-0.1 dB	± 0.5 dB
114dB	-0.3 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The equipment does comply with specification limit.

Checked by : 
CA-R-297 (22/07/2009)

Date : 4.3.2016

Certified by : 

Date : 07 MAR 2016

Kwok Chi Wa (Assistant Manager)

** End of Report **

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.materialab.com

MaterialLab

Report no.: 161966CA160797

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : MaterialLab Consultants Ltd.

Address : Room 723 & 725, 7F., Block B Profit Industrial Building, 1-15 Kwai Fung Crescent, Kwai Chung, N.T.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
Manufacturer : Casella (Model no. CEL-120/1)
Serial No. : 5230736
Next Calibration Date : 20-Apr-2017
Specification Limit : $\pm 0.5\text{dB}$

Laboratory Information



Description : Reference Sound Level Meter
Equipment ID. : R-119-1
Date of Calibration : 21-Apr-2016 Ambient Temperature : 21 °C
Calibration Location : Calibration Laboratory of MaterialLab
Method Used : By direct comparison

Calibration Results :

Parameters (Setting of UUT)	Mean of Measured value	Specification Limit(dB)
94dB	93.9 dB	$\pm 0.5\text{dB}$
114dB	114.1 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The equipment does comply with specification limit.

Checked by :  Date : 22/4/2016 Certified by :  Date : 22 APR 2016
CA-R-297 (22/07/2009) Kwok Chi Wa (Assistant Manager)

** End of Report **

Certificate of
Conformance and Calibration for

CEL-120 Acoustic Calibrator

Applicable Standards :- IEC 60942: 2003 & ANSI S1.40: 2006

CEL-120/1 Class 1

CEL-120/2 Class 2

Serial No: 4358251

Firmware: 03

Temperature: 22.0 °C Pressure: 999.5 mb %RH 55.0

Frequency = 1.00kHz ± 2Hz T.H.D. = < 1%	Calibration Level
SPL @ 114.0dB Setting	<u>113.99</u> dB
SPL @ 94.0dB Setting (CEL-120/1 only)	<u>93.93</u> dB/N.A

Engineer :- M. Duncanson Date :- 12 MAY 2016

Company test equipment and acoustic working standards, used for conformance testing, are subject to periodic calibration, traceable to UK national standards, in accordance with the company's ISO9001 Quality System.

DECLARATION OF CONFORMITY

This certificate confirms that the instrument specified above has been produced and tested to comply with the manufacturer's published specifications and the relevant European Community CE directives.

Casella CEL (U.K.),
Regent House, Wolsley Road, Kempston, Bedford, MK42 7JY
Phone: +44 (0) 1234 844100 Fax: +44 (0) 1234 841490
E-mail: info@casellacel.com
Web: www.casellameasurement.com

198032A-01

Certificate of Conformity and Calibration

Instrument Model:- CEL-633A
 Serial Number 3756127
 Firmware revision V129-09

Microphone Type:- CEL-251
 Serial Number 1231

Preamplifier Type:- CEL-495
 Serial Number 003036

Instrument Class/Type:- 1



Applicable standards:-

IEC 61672: 2002 / EN 60651 (Electroacoustics - Sound Level Meters)
 IEC 60651 1979 (Sound Level Meters), ANSI S1.4: 1983 (Specifications For Sound Level Meters)

Note:- The test sequences performed in this report are in accordance with the current Sound level meter Standard - IEC61672. The combination of tests performed are considered to confirm the products electro-acoustic performance to all applicable standards including superceeded Sound Level Meter Standards - IEC60651 and IEC60804.

Test Conditions:- 25 °C
 52 %RH
 1010 mBar

Test Engineer:- Millie Duncan
Date of Issue:- February 2, 2016

Declaration of conformity:-

This test certificate confirms that the instrument specified above has been successfully tested to comply with the manufacturer's published specifications. Tests are performed using equipment traceable to national standards in accordance with Casella's ISO 9001:2008 quality procedures. This product is certified as being compliant to the requirements of the CE Directive.

Test Summary:-


- Self Generated Noise Test
- Electrical Signal Test Of Frequency Weightings
- Frequency & Time Weightings At 1 kHz
- Level Linearity On The Reference Level Range
- Toneburst Response Test
- C-peak Sound Levels
- Overload Indication
- Acoustic Tests

- All Tests Pass
- All Tests Pass
- All Tests Pass
- All Tests Pass
- All Tests Pass
- All Tests Pass
- All Tests Pass
- All Tests Pass

Combined Electro-Acoustic Frequency Response - A Weighted

Combined Electro-Acoustic Frequency Response - A Weighted (IEC 61672-3:2006)

The following A-Weighted frequency response graph shows this instruments overall frequency response based upon the application of multi-frequency pressure field calibrations. The microphones Pressure to Free field correction coefficients are applied to pressure response. Reference level taken at 1kHz.

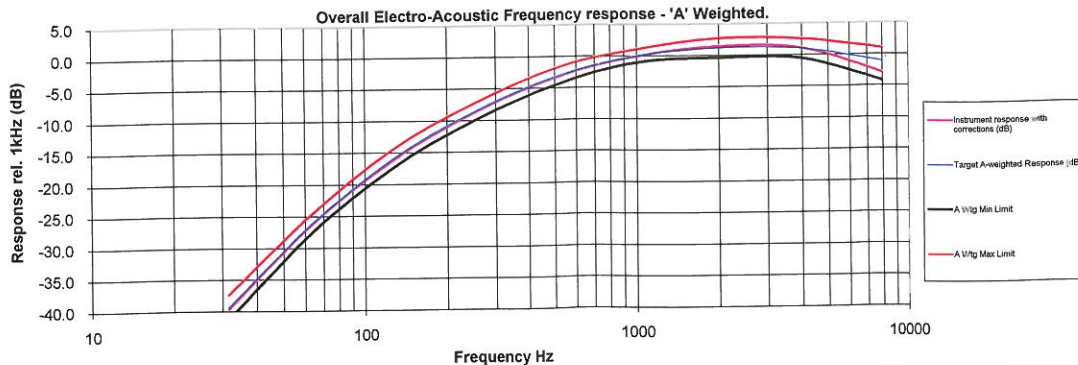

Casella CEL
 Regen House, Wolsley Road,
 Kempston, Bedford
 MK42 7JY
 Phone: +44(0) 1234 844100
 Fax: +44(0) 1234 841490
 E-mail: info@casellameasurement.com
 Web: www.casellameasurement.com

Casella CEL, Inc. a subsidiary of IDEAL Industries, Inc.
 415 Lawrence Bell Drive
 Unit 4
 Buffalo, NY 14221
 Toll Free: (800) 366-2966
 Tel: (603) 672-0031 Fax: (603) 672-8053
 E-mail: info@casellausa.com
 Web: www.casellausa.com

Certificate of Conformity and Calibration

Instrument Model:-	CEL-633A		
Serial Number	3756084		
Firmware revision	V129-09		
Microphone Type:-	CEL-251	Preamplifier Type:-	CEL-495
Serial Number	1257	Serial Number	003538
Instrument Class/Type:-	1		



Applicable standards:-

IEC 61672: 2002 / EN 60651 (Electroacoustics - Sound Level Meters)
 IEC 60651 1979 (Sound Level Meters), ANSI S1.4: 1983 (Specifications For Sound Level Meters)

Note:- The test sequences performed in this report are in accordance with the current Sound level meter Standard - IEC61672. The combination of tests performed are considered to confirm the products electro-acoustic performance to all applicable standards including superceded Sound Level Meter Standards - IEC60651 and IEC60804.

Test Conditions:-	25 °C	Test Engineer:-	Millie Duncan
	52 %RH	Date of Issue:-	February 2, 2016
	1010 mBar		

Declaration of conformity:-

This test certificate confirms that the instrument specified above has been successfully tested to comply with the manufacturer's published specifications. Tests are performed using equipment traceable to national standards in accordance with Casella's ISO 9001:2008 quality procedures. This product is certified as being compliant to the requirements of the CE Directive.


Test Summary:-

Self Generated Noise Test	All Tests Pass
Electrical Signal Test Of Frequency Weightings	All Tests Pass
Frequency & Time Weightings At 1 kHz	All Tests Pass
Level Linearity On The Reference Level Range	All Tests Pass
Toneburst Response Test	All Tests Pass
C-peak Sound Levels	All Tests Pass
Overload Indication	All Tests Pass
Acoustic Tests	All Tests Pass

Combined Electro-Acoustic Frequency Response - A Weighted

Combined Electro-Acoustic Frequency Response - A Weighted (IEC 61672-3:2006)

The following A-Weighted frequency response graph shows this instruments overall frequency response based upon the application of multi-frequency pressure field calibrations. The microphones Pressure to Free field correction coefficients are applied to pressure response. Reference level taken at 1kHz.

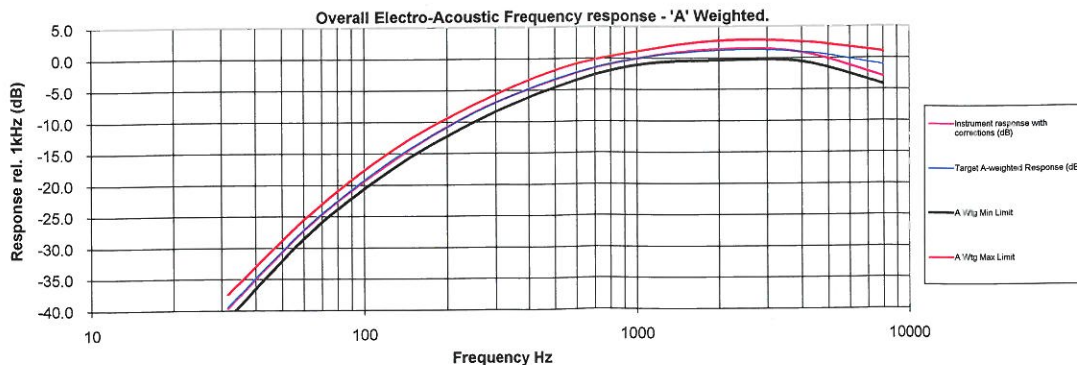

Casella CEL
 Regen House, Wolseley Road,
 Kempston, Bedford
 MK42 7JY
 Phone: +44(0) 1234 844100
 Fax: +44(0) 1234 841490
 E-mail: info@casellameasurement.com
 Web: www.casellameasurement.com

Casella CEL, Inc. a subsidiary of IDEAL Industries, Inc.
 415 Lawrence Bell Drive
 Unit 4
 Buffalo, NY 14221
 Toll Free: (800) 366-2966
 Tel: (603) 672-0031 Fax: (603) 672-8053
 E-mail: info@casellausa.com
 Web: www.casellausa.com

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report no.: 940891CA152019(1)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Level Meter
Manufacturer : Casella (Model no. CEL-63X(meter), CEL-251(microphone), CEL-495(Preamplifier))
Serial No. : 3321823 (meter), 2058 (microphone), 001598 (Preamplifier)
Next Calibration Date : 14-Oct-2016
Specification Limit : EN 60651: 1994 Type 1

Laboratory Information


Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)
Equipment ID. : R-108-1
Date of Calibration : 15-Oct-2015 Ambient Temperature : 20 °C
Calibration Location : Calibration Laboratory of Materialab
Method Used : By direct comparison

Calibration Results :

Parameters		Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	0.6	2.0 to 0.0
	2000Hz	1.1	2.2 to 0.2
	1000Hz	0.0	1.0 to -1.0
	500Hz	-3.2	-2.2 to -4.2
	250Hz	-8.6	-7.6 to -9.6
	125Hz	-16.0	-15.1 to -17.1
	63Hz	-26.0	-24.7 to -27.7
	31.5Hz	-38.9	-37.9 to -40.9
Differential level linearity	94dB-104dB	0.0	± 0.4
	104dB-114dB	0.1	± 0.4

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighing is fast
4. The equipment does comply with EN 60651: 1994 Type 1 sound level meter for the above measurement.

Checked by : 
CA-R-297 (22/07/2009)

Date : 15/10/2015

Certified by : 

So Chi Kuen (Engineer)

Date : 15 Oct, 2015

** End of Report **

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix E

Environmental Monitoring Schedule

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong.

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

**Project: KL/2014/03 - Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway****Impact Monitoring Schedule (June 2016)**

Sun	Mon	Tue	Wed	Thur	Fri	Sat
			1 June 2016	2 TSP Monitoring Noise Monitoring	3	4
5	6	7	8 TSP Monitoring Noise Monitoring	9	10	11
12	13	14 TSP Monitoring Noise Monitoring	15	16	17	18
19	20 TSP Monitoring Noise Monitoring	21	22	23	24	25 TSP Monitoring Noise Monitoring
26	27	28	29	30 TSP Monitoring Noise Monitoring		

Remarks

1. Monitoring Locations – KTD1a: Centre of Excellence in Paediatric (Children's Hospital), KTD2a: G/IC Zone next to Kwun Tong Bypass (Future at Site 3C1), KER1a: Site Boundary at Cheung Yip Street
2. TSP Monitoring: 24-hours TSP Monitoring per 6 days, and 3 x 1-hour TSP Monitoring per 6 days (as required in case of complaints)
3. Noise Monitoring: Leq (30 min) between 0700 and 1900 hours.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong.

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk



Project: KL/2014/03 - Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

Impact Monitoring Schedule (July 2016)

Sun	Mon	Tue	Wed	Thur	Fri	Sat
					1 July 2016	2
3	4	5	6 TSP Monitoring Noise Monitoring	7	8	9
10	11	12 TSP Monitoring Noise Monitoring	13	14	15	16
17	18 TSP Monitoring Noise Monitoring	19	20	21	22	23 TSP Monitoring Noise Monitoring
24	25	26	27	28	29 TSP Monitoring Noise Monitoring	30
31						

Remarks

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition
- Monitoring Locations – KTD1a: Centre of Excellence in Paediatric (Children’s Hospital), KTD2a: G/IC Zone next to Kwun Tong Bypass (Future at Site 3C1), KER1a: Site Boundary at Cheung Yip Street
- TSP Monitoring: 24-hours TSP Monitoring per 6 days, and 3 x 1-hour TSP Monitoring per 6 days (as required in case of complaints)
- Noise Monitoring: Leq (30 min) between 0700 and 1900 hours.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong.

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk



Project: KL/2014/03 - Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

Impact Monitoring Schedule (August 2016)

Sun	Mon	Tue	Wed	Thur	Fri	Sat
	1 August 2016	2	3	4 TSP Monitoring Noise Monitoring	5	6
7	8	9	10 TSP Monitoring Noise Monitoring	11	12	13
14	15	16 TSP Monitoring Noise Monitoring	17	18	19	20
21	22 TSP Monitoring Noise Monitoring	23	24	25	26	27 TSP Monitoring Noise Monitoring
28	29	30	31			

Remarks

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition
- Monitoring Locations – KTD1a: Centre of Excellence in Paediatric (Children's Hospital), KTD2a: G/IC Zone next to Kwun Tong Bypass (Future at Site 3C1), KER1a: Site Boundary at Cheung Yip Street
- TSP Monitoring: 24-hours TSP Monitoring per 6 days, and 3 x 1-hour TSP Monitoring per 6 days (as required in case of complaints)
- Noise Monitoring: Leq (30 min) between 0700 and 1900 hours.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong.

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab**Project: KL/2014/03 - Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway****Impact Monitoring Schedule (September 2016)**

Sun	Mon	Tue	Wed	Thur	Fri	Sat
				1 September 2016	2 TSP Monitoring Noise Monitoring	3
4	5	6	7	8 TSP Monitoring Noise Monitoring	9	10
11	12	13	14 TSP Monitoring Noise Monitoring	15	16	17
18	19	20 TSP Monitoring Noise Monitoring	21	22	23	24
25	26 TSP Monitoring Noise Monitoring	27	28	29	30 TSP Monitoring Noise Monitoring	

Remarks

1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition
2. Monitoring Locations – KTD1a: Centre of Excellence in Paediatric (Children's Hospital), KTD2a: G/IC Zone next to Kwun Tong Bypass (Future at Site 3C1), KER1a: Site Boundary at Cheung Yip Street
3. TSP Monitoring: 24-hours TSP Monitoring per 6 days, and 3 x 1-hour TSP Monitoring per 6 days (as required in case of complaints)
4. Noise Monitoring: Leq (30 min) between 0700 and 1900 hours.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix F

Air Quality Monitoring Data

**24-hour TSP Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD1a - Centre of Excellence in Paediatrics (Children's Hospital)

Start Date	Weather Condition	Air Temperature (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Sampling Time(hrs)	Flow Rate (m ³ /min.)		Average flow (m ³ /min.)	Total volume (m ³)	Conc. (ug/m ³)	Action Level (ug/m ³)	Limit Level (ug/m ³)
				Initial	Final			Initial	Final					
2-Jun-16	Sunny	303.3	754.6	2.7360	2.7996	0.0636	24	0.95	0.96	0.95	1371.9	46	177	260
8-Jun-16	Fine	300.1	754.8	2.6896	2.7967	0.1071	24	1.10	1.11	1.11	1596.3	67		
14-Jun-16	Fine	303.2	753.2	2.7982	2.8763	0.0781	24	0.94	0.96	0.95	1367.1	57		
20-Jun-16	Sunny	303.8	756.4	2.8035	2.9511	0.1476	24	1.07	1.08	1.07	1545.5	96		
25-Jun-16	Fine	304.4	756.7	2.9172	3.1982	0.2810	24	1.31	1.33	1.32	1922.5	146		
30-Jun-16	Fine	303.0	757.8	2.7236	2.8309	0.1073	24	1.16	1.21	1.18	1702.9	63		
												Min	46	
												Max	146	
												Average	79	

KTD2a - G/I/C Zone next to Kwun Tong Bypass (Future Hospital at Site 3C1)

Start Date	Weather Condition	Air Temperature (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Sampling Time(hrs)	Flow Rate (m ³ /min.)		Average flow (m ³ /min.)	Total volume (m ³)	Conc. (ug/m ³)	Action Level (ug/m ³)	Limit Level (ug/m ³)
				Initial	Final			Initial	Final					
2-Jun-16	Sunny	303.3	754.6	2.7479	2.8344	0.0865	24	1.43	1.45	1.44	2076.5	42	157	260
8-Jun-16	Fine	300.1	754.8	2.6864	2.7819	0.0955	24	1.55	1.52	1.53	2208.6	43		
14-Jun-16	Fine	303.2	753.2	2.8128	2.9485	0.1357	24	1.47	1.49	1.48	2126.0	64		
20-Jun-16	Sunny	303.8	756.4	2.8131	2.9507	0.1376	24	1.43	1.45	1.44	2076.9	66		
25-Jun-16	Fine	304.4	756.7	2.9269	3.0387	0.1118	24	1.50	1.52	1.51	2176.7	51		
30-Jun-16	Fine	303.0	757.8	2.7254	2.8084	0.0830	24	1.47	1.49	1.48	2129.8	39		
												Min	39	
												Max	66	
												Average	51	




KER1a - Site Boundary at Cheung Yip Street

Start Date	Weather Condition	Air Temperature (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Sampling Time(hrs)	Flow Rate (m ³ /min.)		Average flow (m ³ /min.)	Total volume (m ³)	Conc. (ug/m ³)	Action Level (ug/m ³)	Limit Level (ug/m ³)
				Initial	Final			Initial	Final					
2-Jun-16	Sunny	303.3	754.6	2.7528	2.8379	0.0851	24	1.10	1.11	1.11	1604.3	53	172	260
8-Jun-16	Fine	300.1	754.8	2.6824	2.7382	0.0558	24	1.08	1.09	1.08	1569.3	36		
14-Jun-16	Fine	303.2	753.2	2.8093	2.8962	0.0869	24	0.99	1.01	1.00	1482.5	59		
20-Jun-16	Sunny	303.8	756.4	2.8175	2.8466	0.0291	24	1.05	1.01	1.03	1495.3	19		
25-Jun-16	Fine	304.4	756.7	2.9311	2.9732	0.0421	24	1.00	1.01	1.00	1448.5	29		
30-Jun-16	Fine	303.0	757.8	2.7294	2.7754	0.0460	24	1.00	1.01	1.00	1469.5	31		
												Min	19	
												Max	59	
												Average	38	

Note:

Underline: Exceedance of Action Level

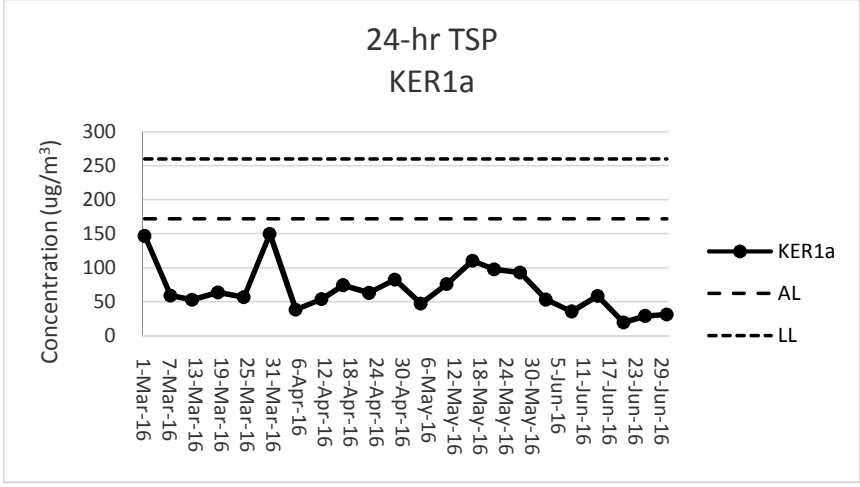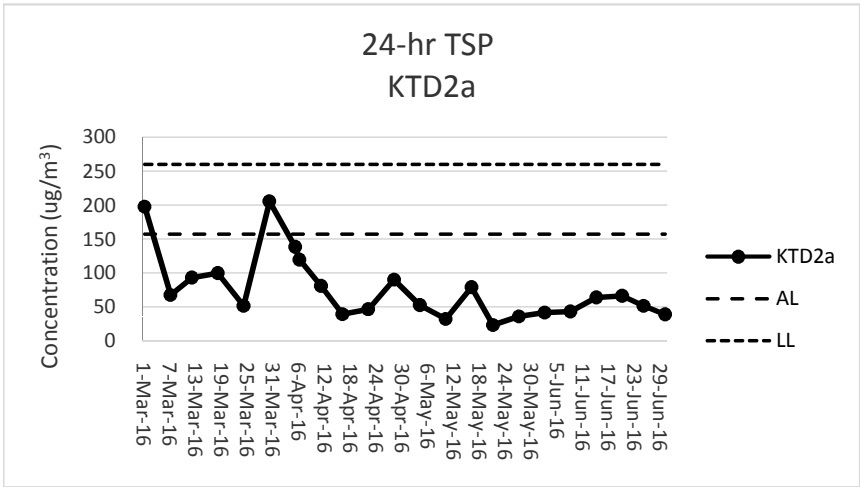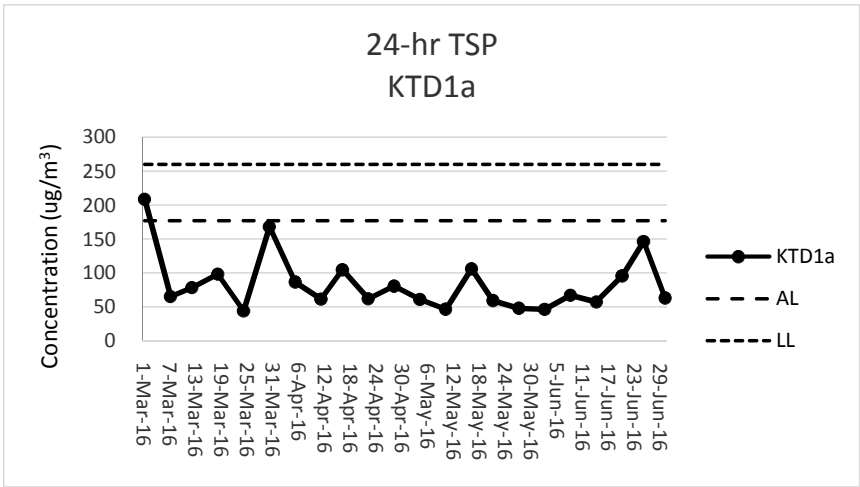Underline and Bold: Exceedance of Limit Level



- Note:
- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
 - 2) The weather conditions during the reporting period can be referred to Appendix K.
 - 3) Any other factors which might affect the monitoring results can be referred to Section 2.6.4.
 - 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, sans-serif font. The text is white and is set against a black rectangular background that has horizontal bars extending to the left and right, creating a stylized, framed effect.

Appendix G

Noise Monitoring Data

**Noise Impact Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD 1a: Centre of Excellence in Paediatrics (Children's Hospital)

Date	Start Time	Leq 30min dB(A)	Wind Speed (m/s)	Weather
2-Jun-16	12:38	60	0.5	Sunny
8-Jun-16	9:27	70	0.0	Fine
14-Jun-16	10:10	72	0.4	Fine
20-Jun-16	10:21	66	1.3	Sunny
25-Jun-16	10:40	67	0.0	Fine
30-Jun-16	10:46	68	0.0	Fine
Max		72		
Min		60		
Limit Level		75		

KTD 2a: G/I/C Zone next to Kwun Tong Bypass (Future Hospital at Site 3C1)

Date	Start Time	Leq 30min dB(A)	Wind Speed (m/s)	Weather
2-Jun-16	12:05	63	0.6	Sunny
8-Jun-16	10:04	62	0.0	Fine
14-Jun-16	10:57	63	0.5	Fine
20-Jun-16	9:35	59	1.5	Sunny
25-Jun-16	11:21	59	1.3	Fine
30-Jun-16	11:27	60	0.8	Fine
Max		63		
Min		59		
Limit Level		75		

KER 1a: Site Boundary at Cheung Yip Street




Date	Start Time	Leq 30min dB(A)	Wind Speed (m/s)	Weather
2-Jun-16	13:18	69	0.5	Sunny
8-Jun-16	8:43	67	0.0	Fine
14-Jun-16	9:25	70	0.4	Fine
20-Jun-16	11:00	67	1.5	Sunny
25-Jun-16	10:07	68	1.8	Fine
30-Jun-16	10:09	69	1.3	Fine
Max		70		
Min		67		
Limit Level		75		

Note:

KTD1a: Façade Measurement

KTD2a & KER1a: Free-field measurement (+3dB(A) correction has been applied)

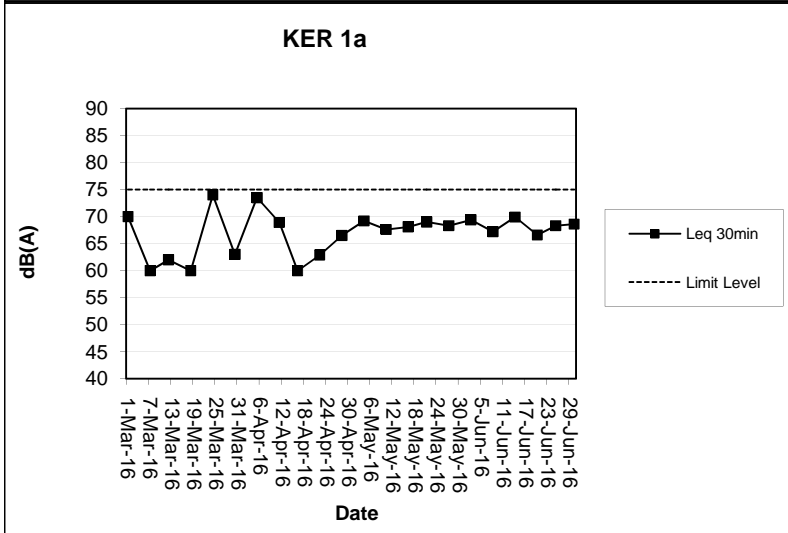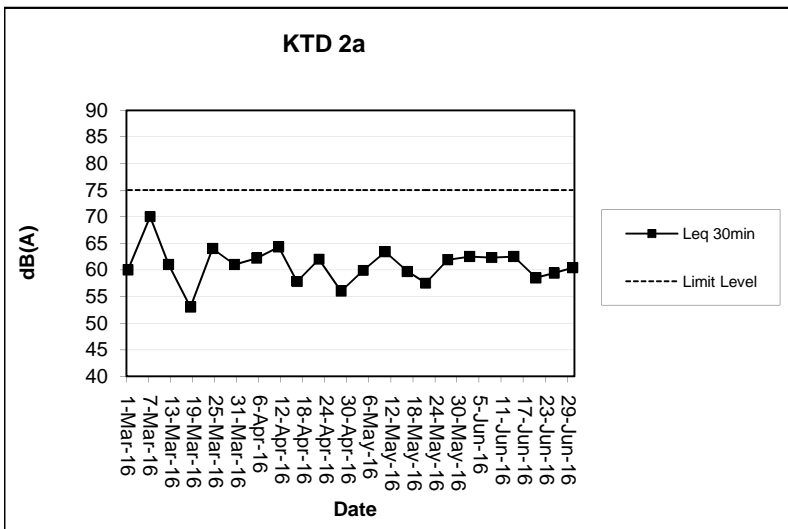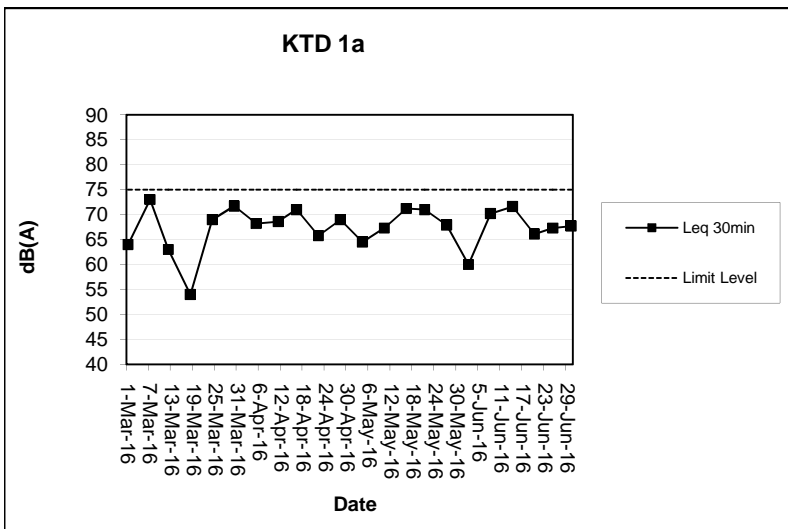No raining or wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.



Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
- 2) The weather conditions during the reporting period can be referred to Appendix K.
- 3) Any other factors which might affect the monitoring results can be referred to Section 3.7.2.
- 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix H

Events and Action Plan

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk



Event and Action Plan for Construction Dust Monitoring

EVENT	ACTION			
	ET	IEC	ER	Contractor
Action Level				
Exceedance for one sample.	<ol style="list-style-type: none"> 1. Identify sources, investigate the causes of complaint and propose remedial measures. 2. Inform IEC and ER. 3. Repeat measurement to confirm finding;. 4. Increase monitoring frequency 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods. 	<ol style="list-style-type: none"> 1. Notify the Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practices. 2. Amend working methods agreed with the ER as appropriate.
Exceedance for two or more consecutive samples.	<ol style="list-style-type: none"> 1. Identify sources. 2. Inform the IEC and ER. 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings. 5. Increase monitoring frequency to daily. 6. Discuss with the IEC, ER and Contractor on remedial action required. 7. If exceedance continues, arrange meeting with the IEC, Contractor and ER. 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods. 3. Discuss with the ET, ER and Contractor on possible remedial measures if required. 4. Advise the ER on the effectiveness of proposed remedial measures if required. 	<ol style="list-style-type: none"> 1. Notify the Contractor. 2. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial action to the ER within 3 working days of notification. 2. Implement the agreed proposals. 3. Amend proposal as appropriate
Limit Level				
Exceedance for one sample.	<ol style="list-style-type: none"> 1. Identify sources, investigate causes of exceedance and proposed remedial measures. 2. Inform the IEC, ER, and Contractor. 3. Repeat measurement to confirm finding. 4. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of the Contractor's remedial action and keep the IEC and ER informed of the results 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check the Contractor's working methods. 3. Discuss with the ET, ER and Contractor on possible remedial measures. 4. Advise the ER and ET on the effectiveness of the proposed remedial measures. 5. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of the notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial action to the ER and copy to the ET and IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Amend proposal as appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify the IEC, ER and Contractor. 2. Identify sources. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures with the ER to determine the possible mitigation to be implemented. 6. Arrange meeting with the IEC and ER to 	<ol style="list-style-type: none"> 1. Discuss amongst the ER, ET and Contractor on the potential remedial action. 2. Review the Contractor's remedial action whenever necessary to assure their effectiveness and advise the ER and ET accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of the notification of exceedance in writing. 2. Notify the Contractor. 3. In consultation with the IEC and ET, agree with the Contractor on the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial action to the ER and copy to the IEC and ET within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problems still not under control. 5. Stop the relevant portion of works as

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars.

EVENT	ACTION			
	ET	IEC	ER	Contractor
	<p>discuss the remedial action to be taken.</p> <p>7. Assess the effectiveness of the Contractor's remedial action and keep the IEC, EPD and ER informed of the results.</p> <p>8. If exceedance stops, cease additional monitoring</p>		<p>continues, consider what portion of works is responsible and instruct the Contractor to stop that portion of works until the exceedance is abated.</p>	<p>determined by the ER until the exceedance is abated.</p>

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk



Event and Action Plan for Noise Impact

EVENT	ACTION			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify the IEC, ER and Contractor. 2. Carry out investigation. 3. Report the results of investigation to the IEC and Contractor. 4. Discuss jointly with the ER and Contractor and formulate remedial measures. 5. Increase the monitoring frequency to check the mitigation effectiveness 	<ol style="list-style-type: none"> 1. Review the monitoring data submitted by the ET. 2. Review the construction methods and proposed remedial measures by the Contractor, and advise the ET and ER if the proposed remedial measures would be sufficient 	<ol style="list-style-type: none"> 1. Notify the Contractor. 2. Require the Contractor to propose remedial measures for implementation if required. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to the ER and copy to the IEC and ET. 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Notify the IEC, ER and Contractor. 2. Identify sources. 3. Repeat measurements to confirm findings. 4. Carry out analysis of the Contractor's working procedures with the ER and Contractor to determine possible mitigations to be implemented. 5. Record the causes and action taken for the exceedances. 6. Increase the monitoring frequency. 7. Assess the effectiveness of the Contractor's remedial action with the ER and keep the IEC informed of the results. 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst the ER, ET and Contractor on the potential remedial action. 2. Review the Contractor's remedial action whenever necessary to assure their effectiveness and advise the ER accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problems. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what portion of work is responsible and instruct the Contractor to stop that portion of works until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial action to the ER and copy to the ET and IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problems still not under control. 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk



Event and Action Plan for Landscape and Visual Impact

EVENT	ACTION			
	ET	IEC	ER	Contractor
Non-conformity on one occasion	<ol style="list-style-type: none">1. Identify Source2. Inform the IEC and the ER3. Discuss remedial actions with the IEC, the ER and the Contractor4. Monitor remedial actions until rectification has been completed	<ol style="list-style-type: none">1. Check report2. Check the Contractor's working method3. Discuss with the ET and the Contractor on possible remedial measures4. Advise the ER on effectiveness of proposed remedial measures.5. Check implementation of remedial measures.	<ol style="list-style-type: none">1. Notify Contractor2. Ensure remedial measures are properly implemented	<ol style="list-style-type: none">1. Amend working methods2. Rectify damage and undertake any necessary replacement
Repeated Non-conformity	<ol style="list-style-type: none">1. Identify Source2. Inform the IEC and the ER3. Increase monitoring frequency4. Discuss remedial actions with the IEC, the ER and the Contractor5. Monitor remedial actions until rectification has been completed6. If exceedance stops, cease additional monitoring	<ol style="list-style-type: none">1. Check monitoring report2. Check the Contractor's working method3. Discuss with the ET and the Contractor on possible remedial measures4. Advise the ER on effectiveness of proposed remedial measures5. Supervise implementation of remedial measures.	<ol style="list-style-type: none">1. Notify the Contractor2. Ensure remedial measures are properly implemented	<ol style="list-style-type: none">1. Amend working methods2. Rectify damage and undertake any necessary replacement

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix I

Waste Flow Table

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

MaterialLab

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2016 Jan	0.159	0.101	0.058	Nil	Nil	Nil	Nil	0.023	0.00002	0.0158	0.0335
2016 Feb	0.291	0.050	0.241	Nil	Nil	Nil	1.34	0.023	0.00002	0.0158	0.0335
2016 Mar	2.7389	0.0407	0.0662	Nil	2.632	Nil	5.92	0.023	0.00002	0.0158	0.0571
2016 Apr	4.1718	0.0578	0.462	Nil	3.652	Nil	12.5	0.023	0.00002	0.0158	0.0426
2016 May	3.592	Nil	0.299	Nil	3.293	Nil	5.23	0.023	0.00002	0.0158	0.0621
2016 June	4.6035	Nil	0.8555	Nil	3.748	Nil	Nil	0.023	0.00002	0.0158	0.0619
2016 July											
2016 Aug											
2016 Sept											
2016 Oct											
2016 Nov											
2016 Dec											
Total	15.5562	0.2495	1.9817	Nil	13.325	Nil	24.99	0.138	0.00012	0.0948	0.2907

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix J

Environmental Mitigation Implementation Schedule (EMIS)

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
<u>Air Quality Measures</u>					
New Distributor Roads Serving the Planned KTD					
AEIAR-130/2009 S3.2	AEIAR 130/2009 EM&A Manual S2.2	8 times daily watering of the work site with active dust emitting activities.	Contractor	All relevant worksites	Implemented
Decommissioning of the Radar Station of the former Kai Tak Airport					
AEIAR-130/2009 S5.2.19	AEIAR 130/2009 EM&A Manual S4.2.4	The excavation area should be limited to as small in size as possible and backfilled with clean and/or treated soil shortly after excavation work. The exposed excavated area should be covered by the tarpaulin during night time. The top layer soils should be sprayed with fine misting of water immediately before the excavation.	Contractor	All relevant worksites	Not Applicable
Trunk Road T2					
AEIAR-174/2013 S4.9.2.1	AEIAR-174/2013 EM&A Manual S2.3.1.1	Watering of the construction areas 12 times per day to reduce dust emissions by 91.7%, with reference to the "Control of Open Fugitive Dust Sources" (USEPA AP-42). The amount of water to be applied would be 0.91L/m ² for the respective watering frequency.	Contractor	All relevant worksites	Implemented
		Dust enclosures with watering would be provided along the loading ramps and conveyor belts for unloading the C&D materials to the barge for dust suppression.	Contractor	All relevant worksites	Not Applicable
		8 km per hour is the recommended limit of the speed for vehicles on unpaved site roads.	Contractor	All relevant worksites	Implemented
<u>Good Site Practices</u>					
AEIAR-130/2009	AEIAR 130/2009	Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should	Contractor	All relevant	Partially

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
S3.2, S5.2.19, AEIAR-174/2013 S4.9.2.2	EM&A Manual S2.2, S4.2, AEIAR 174/2013 EM&A Manual S2.3.1.2	be fully covered by impermeable sheeting to reduce dust emission.		worksites	Implemented
		Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent watering for particularly dusty construction areas and areas close to ASRs.	Contractor	All relevant worksites	Implemented
		Misting for the dusty material should be carried out before being loaded into the vehicle. Any vehicle with an open load carrying area should have properly fitted side and tail boards.	Contractor	All relevant worksites	Implemented
		Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.	Contractor	All relevant worksites	Implemented
		Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; The tarpaulin should be properly secured and should extent at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation.	Contractor	All relevant worksites	Implemented
		The vehicles should be restricted to maximum speed of 10 km per hour. Confined haulage and delivery vehicle to designated roadways insider the site. Onsite unpaved roads should be compacted and kept free of lose materials.	Contractor	All relevant worksites	Implemented
		Vehicle washing facilities should be provided at every vehicle exit point. Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.	Contractor	All relevant worksites	Implemented
		The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.			
		Every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.	Contractor	All relevant worksites	Implemented
Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.	Contractor	All relevant worksites	Partially Implemented		

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase
					Implementation Status
		Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.	Contractor	All relevant worksites	Implemented
		Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.	Contractor	All relevant worksites	Implemented
		Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.	Contractor	All relevant worksites	Partially Implemented
		Open stockpiles shall be avoided or covered. Prevent placing dusty material storage piles near ASRs.	Contractor	All relevant worksites	Partially Implemented
		Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs.	Contractor	All relevant worksites	Not Applicable
		<u>Dark smoke</u>			
		Dark smoke emission shall be control in accordance with the Air Pollution Control (Smoke) Regulation and ETWB TCW 19/2005.	Contractor	All relevant worksites	Implemented
		Plant and equipment should be well maintained to prevent dark smoke emission.	Contractor	All relevant worksites	Implemented
<u>Noise Measures</u>					
Trunk Road T2					
AEIAR-174/2013 S5.9.2.1	AEIAR-174/2013 EM&A Manual S3.4.1.1	The use of quieter plant, including Quality Powered Mechanical Equipment (QPME) is specified for the list of equipment: <ul style="list-style-type: none"> • Concrete lorry mixer • Dump Truck, 5.5 tonne < gross vehicle weight <= 38 tonne • Generator, Super Silenced, 70 dB(A) at 7m 	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		<ul style="list-style-type: none"> • Poker, vibratory, Hand-held (electric) • Water Pump, Submersible (Electric) • Mobile Crane - KOBELCO CKS900 • Excavator, wheeled/tracked - HYUNDAI R80CR-9 			
		Use of temporary or fixed noise barriers with a surface density of at least 10kg/m ² to screen noise from movable and stationary plant.	Contractor	All relevant worksites	Not Applicable
		Use of enclosures with covers at top and three sides and a surface density of at least 10kg/m ² to screen noise from generally static noisy plant such as air compressors.	Contractor	All relevant worksites	Not Applicable
		Use of acoustic fabric for the silent piling system, drill rigs, rock drills etc.	Contractor	All relevant worksites	Implemented
		<u>Good Site Practices</u>			
AEIAR-130/2009 S3.3, S5.3.10, AEIAR-174/2013 S5.9.2.1	AEIAR 130/2009 EM&A Manual S2.3, S4.3.2, AEIAR-174/2013 EM&A Manual S3.4.1.1	Only well-maintained plant should be operated on-site and plant shall be serviced regularly during the construction/ decommissioning program.	Contractor	All relevant worksites	Implemented
		Silencers or mufflers on construction equipment should be utilized and shall be properly maintained during the construction/ decommissioning program.	Contractor	All relevant worksites	Not Applicable
		Mobile plant, if any, should be sited as far away from NSRs as possible.	Contractor	All relevant worksites	Implemented
		Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or should be throttled down to a minimum.	Contractor	All relevant worksites	Implemented
		Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Contractor	All relevant worksites	Implemented
		Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction/ decommissioning activities.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Use of site hoarding as a noise barrier to screen noise at low level NSRs.	Contractor	All relevant worksites	Implemented
		For the use of hand held percussive breakers (with mass of above 10kg) and portable air compressors (supply air at 500 kPa or above), the noise level of such PME shall comply with a stringent noise emission standard and a noise emission label shall be obtained from the DEP before use at any time in construction site.	Contractor	All relevant worksites	Implemented
		Quiet powered mechanical equipment (PME) shall be used for the construction of the Project.	Contractor	All relevant worksites	Implemented
		Full enclosures shall be used to screen noise from relatively static PMEs (including air compressor, bar bender, concrete pump, generator and water pump) from sensitive receiver(s).	Contractor	All relevant worksites	Not Applicable
		Movable cantilevered noise barriers shall be used to screen noise from mobile PMEs (including asphalt paver, breaker, excavator and hand-held breaker) from sensitive receiver(s). These movable cantilevered noise barriers shall be located close to the mobile PMEs and shall be moved/adjusted iteratively in step with each movement of the corresponding mobile PMEs in order to maximize their noise reduction effects.	Contractor	All relevant worksites	Not Applicable
		Only approved or exempted Non-road Mobile Machineries (NRMMS) including regulated machines and non-road vehicles with proper labels are allowed to be used in specified activities on-site.	Contractor	All relevant worksites	Implemented
Water Quality Measures					
Trunk Road T2					
		<u>Accidental Spillage</u>			
AEIAR-174/2013 S6.4.8.5	AEIAR-174/2013 EM&A Manual S4.2.1.1	All bentonite slurry should be stored in a container that resistant to corrosion, maintained in good conditions and securely closed; The container should be labelled in English and Chinese and note that the container is for storage of bentonite slurry only.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		The storage container should be placed on an area of impermeable flooring and bunded with capacity to accommodate 110% of the volume of the container size or 20% by volume stored in the area and enclosed with at least 3 sides.	Contractor	All relevant worksites	Implemented
		The storage container should be sufficiently covered to prevent rainfall entering the container or bunded area (water collected within the bund must be tested and disposed of as chemical waste, if necessary). An emergency clean up kit shall be readily available where bentonite fluid will be stored or used.	Contractor	All relevant worksites	Implemented
		The handling and disposal of bentonite slurries should be undertaken in accordance within ProPECC PN 1/94. Surplus bentonite slurries used in construction works shall be reconditioned and reused wherever practicable. Residual bentonite slurry shall be disposed of from the site as soon as possible as stipulated in Clause 8.56 of the General Specification for Civil Engineering Works. The Contractor should explore alternative disposal outlets for the residual bentonite slurry (dewatered bentonite slurry to be disposed to a public filling area and liquid bentonite slurry, if mixed with inert fill material, to be disposed to a public filling area) and disposal at landfill should be the last resort.	Contractor	All relevant worksites	Implemented
AEIAR-174/2013 S6.4.8.8	AEIAR-174/2013 EM&A Manual S4.2.1.1	In order to protect against impacts to the surrounding marine waters of the KTTS and Victoria Harbour in the event of an accidental spillage of fuel or oil, the Contractor will be required to prepare a spill response plan to the satisfaction of AFCD, EPD, FSD, Police, TD and WSD to define procedures for the control, containment and clean-up of any spillage that could occur on the construction site.	Contractor	All relevant worksites	Implemented
		<u>Dredging, Reclamation and Filling</u>			
		No dredging, reclamation or filling in the marine environment shall be carried out.	Contractor	All relevant worksites	Implemented
Decommissioning of the Radar Station of the former Kai Tak Airport					
		<u>Building Demolition</u>			

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
AEIAR-130/2009 S5.4	AEIAR 130/2009 EM&A Manual S4.4	The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed as far as practicable in order to minimise surface runoff and the chance of erosion.	Contractor	All relevant worksites	Not Applicable
		There is a need to apply to EPD for a discharge licence under the WPCO for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge licence. All the runoff, wastewater or extracted groundwater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. It is anticipated that the wastewater generated from the works areas would be of small quantity. Monitoring of the treated effluent quality from the works areas should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD.	Contractor	All relevant worksites	Implemented
		<u>General Construction Works</u>			
		<u>Construction Runoff</u>			
AEIAR-130/2009 S3.4, S5.4/ AEIAR-174/2013 S6.4.8.1	AEIAR 130/2009 EM&A Manual S2.4, S4.4/ AEIAR-174/2013 EM&A Manual S4.2.1.1	Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include the use of sediment traps and adequate maintenance of drainage systems to prevent flooding and overflow.	Contractor	All relevant worksites	Implemented
		Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	Contractor	All relevant worksites	Implemented
		Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.			
		Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	Contractor	All relevant worksites	Implemented
		Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	Contractor	All relevant worksites	Implemented
		Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	Contractor	All relevant worksites	Implemented
		Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.	Contractor	All relevant worksites	Not Applicable
		Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	Contractor	All relevant worksites	Not Applicable
		An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		<u>Drainage</u>			
		It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	Contractor	All relevant worksites	Implemented
		All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	Contractor	All relevant worksites	Partially Implemented
		<u>Stormwater Discharges</u>			
		Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes.	Contractor	All relevant worksites	Not Applicable
		<u>Sewage Effluent</u>			
		Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.	Contractor	All relevant worksites	Implemented
		<u>Debris and Litter</u>			
		In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur. Debris and refuse generated on-site should be collected, handled and disposed of	Contractor	All relevant worksites	Partially Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		properly to avoid entering into the adjacent harbour waters. Stockpiles of cement and other construction materials should be kept covered when not being used.			
		<u>Accidental Spillage</u>			
		Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to the nearby harbour waters, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ. The bund should be drained of rainwater after a rain event.	Contractor	All relevant worksites	Implemented
<u>Waste Management Measures</u>					
		<u>Waste Management Plan</u>			
AEIAR-174/2013 S11.4.8.1	AEIAR-174/2013 EM&A Manual S9.2.1.2	Contractor should be requested to submit an outline Waste Management Plan (WMP) prior to the commencement of construction work, in accordance with the ETWB TC(W) No.19/2005 so as to provide an overall framework of waste management and reduction.	Contractor	All relevant worksites	Implemented
		<u>Good Site Practices</u>			
AEIAR-130/2009 S3.5, S5.5	AEIAR 130/2009 EM&A Manual S2.5, S4.5	Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	Contractor	All relevant worksites	Implemented
		Training of site personnel in proper waste management and chemical waste handling procedures.	Contractor	All relevant worksites	Implemented
		Provision of sufficient waste disposal points and regular collection for disposal.	Contractor	All relevant worksites	Implemented
		Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase
					Implementation Status
		A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Contractor	All relevant worksites	Implemented
		<u>Waste Reduction Measures</u>			
		Sort C&D waste from demolition of the remaining structures to recover recyclable portions such as metals.	Contractor	All relevant worksites	Not Applicable
		Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	Contractor	All relevant worksites	Partially Implemented
		Encourage collection of aluminum cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force.	Contractor	All relevant worksites	Partially Implemented
		Any unused chemicals or those with remaining functional capacity should be recycled.	Contractor	All relevant worksites	Implemented
		Proper storage and site practices to minimize the potential for damage or contamination of construction materials.	Contractor	All relevant worksites	Implemented
		<u>Construction and Demolition Materials</u>			
		Where it is unavoidable to have transient stockpiles of C&D material within the work site pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible.	Contractor	All relevant worksites	Implemented
		Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Contractor	All relevant worksites	Partially Implemented
		Skip hoist for material transport should be totally enclosed by impervious sheeting.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase
					Implementation Status
		Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.	Contractor	All relevant worksites	Implemented
		The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	Contractor	All relevant worksites	Implemented
		The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.	Contractor	All relevant worksites	Implemented
		All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.	Contractor	All relevant worksites	Partially Implemented
		The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.	Contractor	All relevant worksites	Implemented
		When delivering inert C&D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Materials" should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.	Contractor	All relevant worksites	Implemented
		<u>Chemical Waste</u>			
		After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		<u>General Refuse</u>			
		General refuse should be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem.	Contractor	All relevant worksites	Partially Implemented
<u>Land Contamination Measures</u>					
		<u>For any excavation works conducted at Radar Station</u>			
AEIAR-130/2009 S3.6.57	AEIAR 130/2009 EM&A Manual S4.6	As the risk due to dermal contact with groundwater by site workers is uncertain, it is recommended that personnel protective equipment (PPE) be used by site workers as a mitigation measure.	Contractor	All relevant worksites	Not Applicable
<u>Landscape and Visual Impact</u>					
New Distributor Roads Serving the Planned KTD					
		<u>Construction Phase</u>			
AEIAR-130/2009 S3.8.12	AEIAR 130/2009 EM&A Manual S2.8	All existing trees should be carefully protected during construction.	Contractor	All relevant worksites	Not Applicable
		Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.	Contractor	All relevant worksites	Not Applicable
		Control of night-time lighting.	Contractor	All relevant worksites	Not Applicable

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Erection of decorative screen hoarding.	Contractor	All relevant worksites	Implemented
Trunk Road T2					
		<u>Construction Phase</u>			
AEIAR-174/2013 S9.9.1.1	AEIAR-174/2013 EM&A Manual S7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	Contractor	All relevant worksites	Not Applicable
		Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	Contractor	All relevant worksites	Not Applicable
		Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	Contractor	All relevant worksites	Partially Implemented
		Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.	Contractor	All relevant worksites	Implemented
		Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	Contractor	All relevant worksites	Implemented
		All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	Contractor	All relevant worksites	Not Applicable
<u>General Condition</u>					
		The Permit Holder shall display conspicuously a copy of this Permit on the Project site(s) at all vehicular site entrances/exits or at a convenient location for public's information at all times. The Permit Holder shall ensure that the most updated information about the Permit, including any amended Permit, is displayed at such locations. If the Permit Holder surrenders a part or the whole of the Permit, the notice he sends to the Director shall also be displayed at the same	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by MaterialLab Consultants Ltd. It may not be reproduced except with prior written approval from the Company.

A Fugro Group Company

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

Materialab

EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		locations as the original Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site(s).			

Implementation status: Implemented / Partially Implemented / Not Implemented / Not Applicable

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix K

Weather and Meteorological Conditions during Reporting Month

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong..

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk






Date	Mean Pressure (hPa)	Air Temperature			Mean Relative Humidity (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)		
June 2016						
1	1007.8	32.8	30.1	28.6	80	0.0
2	1006.0	33.0	30.3	28.7	79	0.0
3	1006.5	32.4	30.3	29.0	80	Trace
4	1007.9	33.8	28.7	24.7	83	12.4
5	1008.8	30.4	26.9	25.0	86	7.6
6	1008.8	29.1	26.2	24.8	91	77.6
7	1008.1	30.7	28.1	26.3	86	0.4
8	1006.3	30.0	27.1	24.1	89	46.5
9	1005.7	31.7	28.2	26.6	86	Trace
10	1005.7	31.1	27.9	26.6	89	9.1
11	1005.9	27.8	26.6	25.4	93	85.5
12	1005.7	29.2	27.1	25.4	93	28.2
13	1005.0	31.5	29.7	28.5	84	0.1
14	1004.2	31.7	30.2	29.2	81	Trace
15	1005.3	32.0	30.3	29.3	79	0.6
16	1006.7	31.4	29.4	28.2	82	2.8
17	1008.2	32.1	29.4	26.7	82	2.5
18	1010.5	30.8	29.3	27.7	83	13.1
19	1010.3	34.2	30.1	27.8	80	0.0
20	1008.5	34.4	30.8	28.6	78	Trace
21	1009.3	33.7	30.6	28.7	75	0.0
22	1009.5	33.7	30.5	28.5	75	0.0
23	1008.4	34.1	30.4	28.4	72	0.0
24	1008.1	35.2	31.0	28.8	72	0.0
25	1008.9	35.5	31.4	28.9	74	0.0
26	1009.1	35.1	31.3	29.4	75	Trace
27	1007.5	35.1	31.1	28.6	78	1.7
28	1007.5	32.3	29.1	26.3	85	37.1
29	1010.0	33.3	29.0	27.5	87	20.4
30	1010.3	33.1	30.0	27.8	80	1.8


Source: Hong Kong Observatory – Hong Kong Observatory

Wind Speed and Wind Direction Data by Hong Kong Observatory – Kai Tak



Elevation of station: 3m above mean sea level
Elevation of Anemometer: 16m above mean sea level

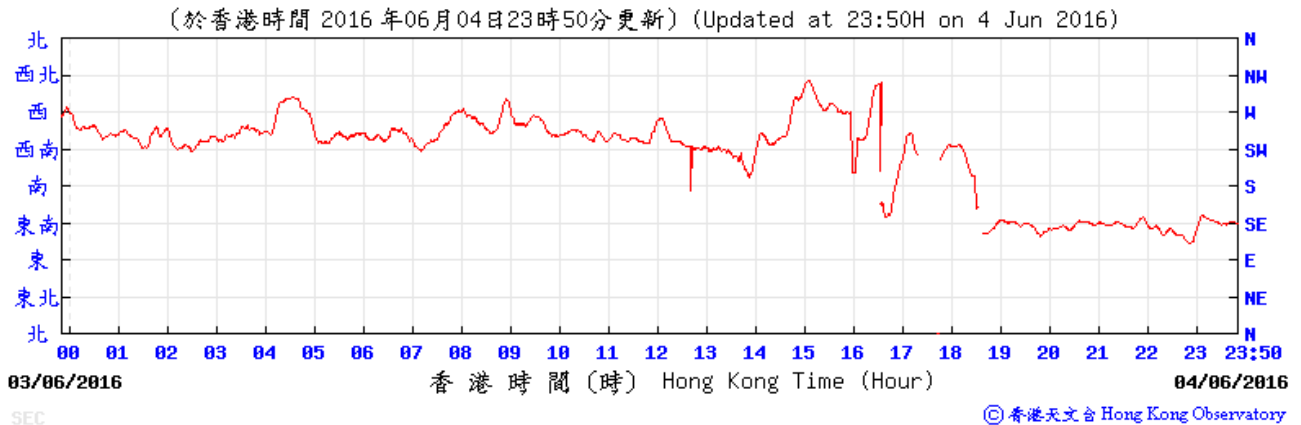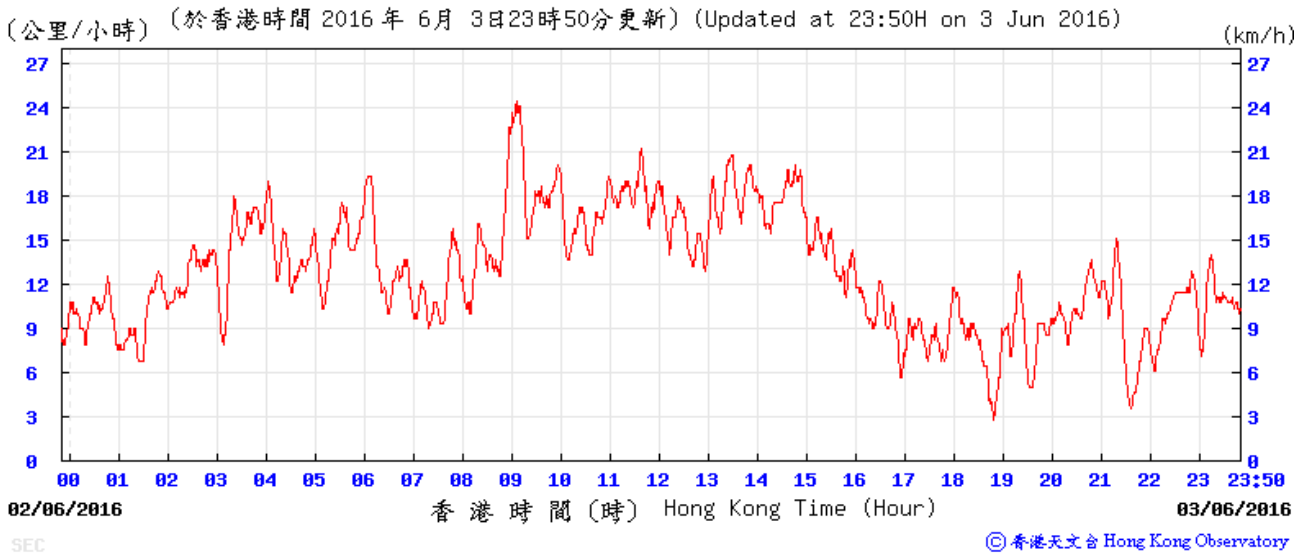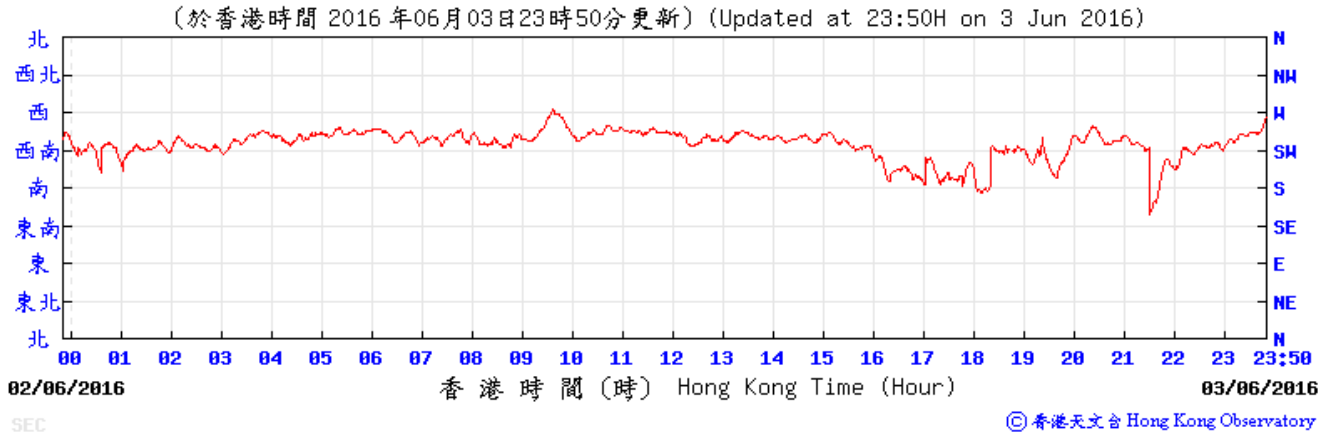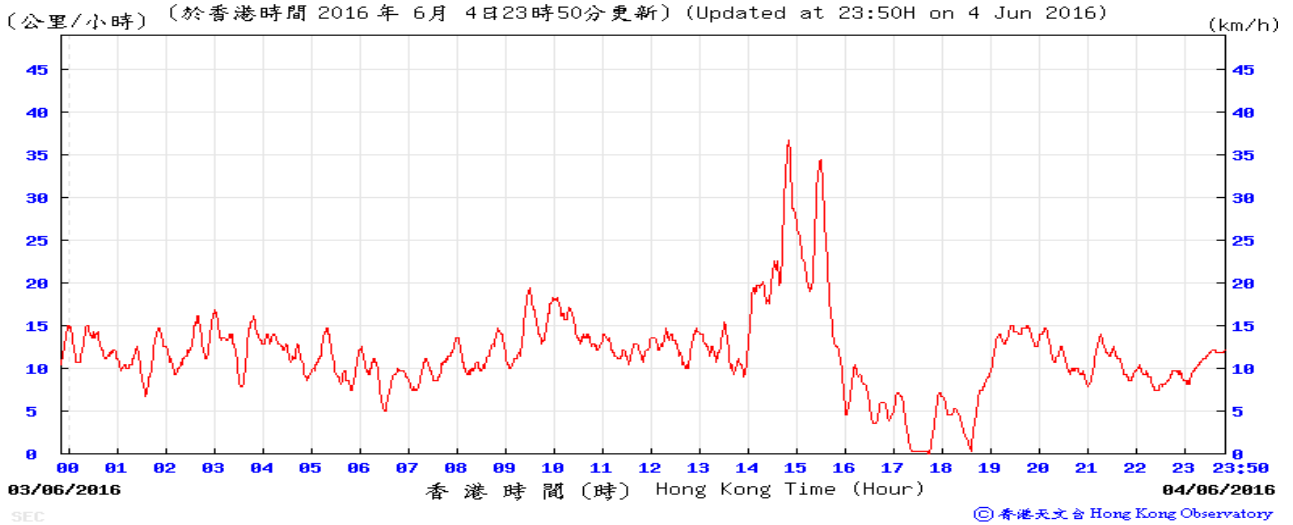2 June 2016 – 3 June 2016







8 June 2016 – 9 June 2016

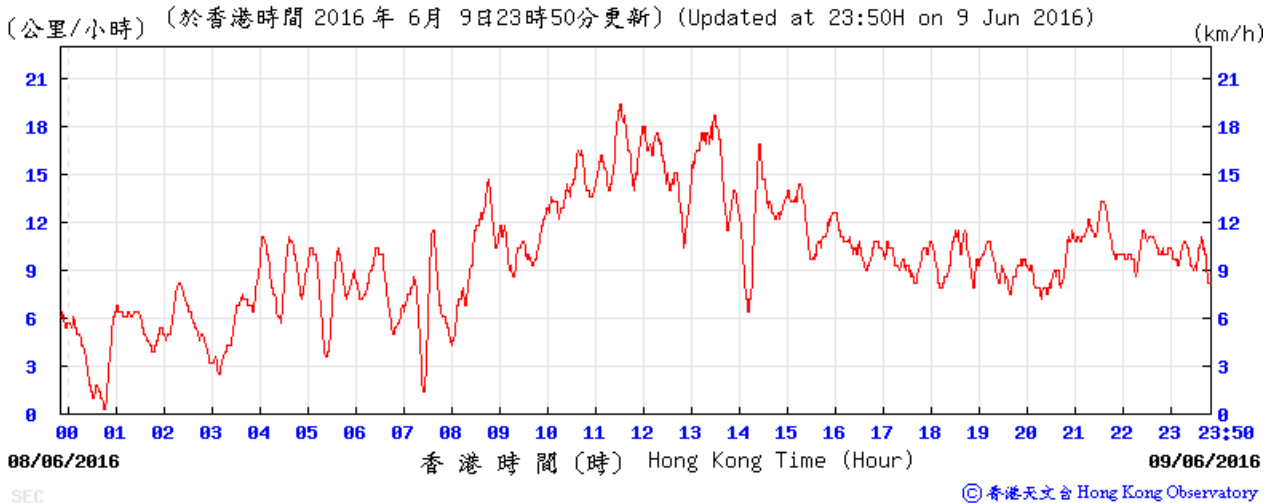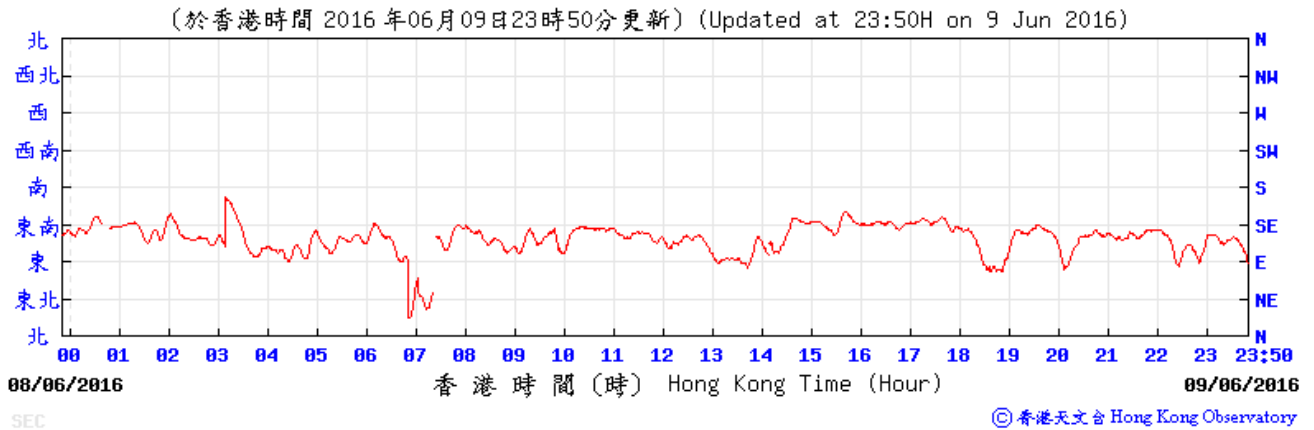

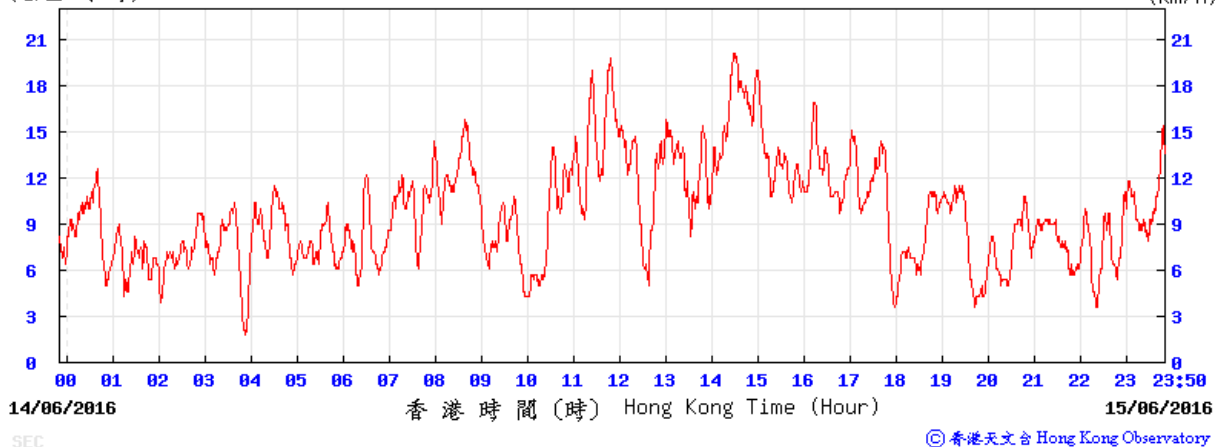
(公里/小時) (於香港時間 2016 年 6 月 15 日 23 時 50 分更新) (Updated at 23:50H on 15 Jun 2016) (km/h)



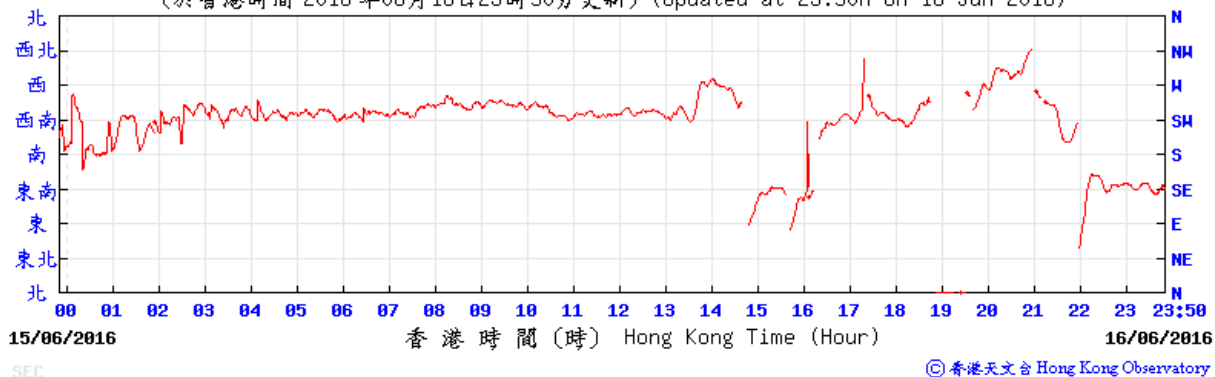(於香港時間 2016 年 06 月 16 日 23 時 50 分更新) (Updated at 23:50H on 16 Jun 2016)



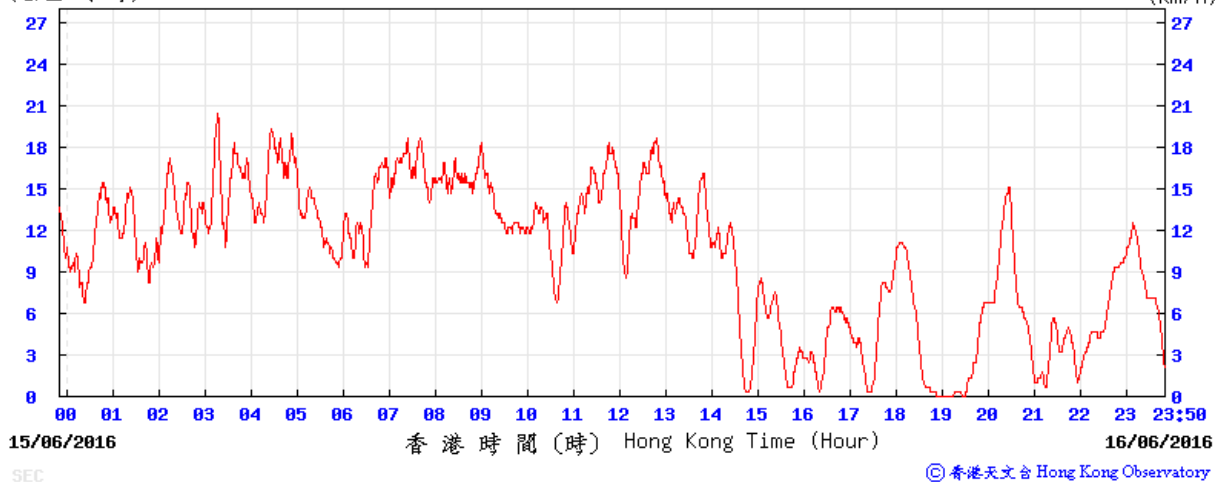(公里/小時) (於香港時間 2016 年 6 月 16 日 23 時 50 分更新) (Updated at 23:50H on 16 Jun 2016) (km/h)




20 June 2016 – 21 June 2016


(於香港時間 2016 年06月21日23時50分更新) (Updated at 23:50H on 21 Jun 2016)



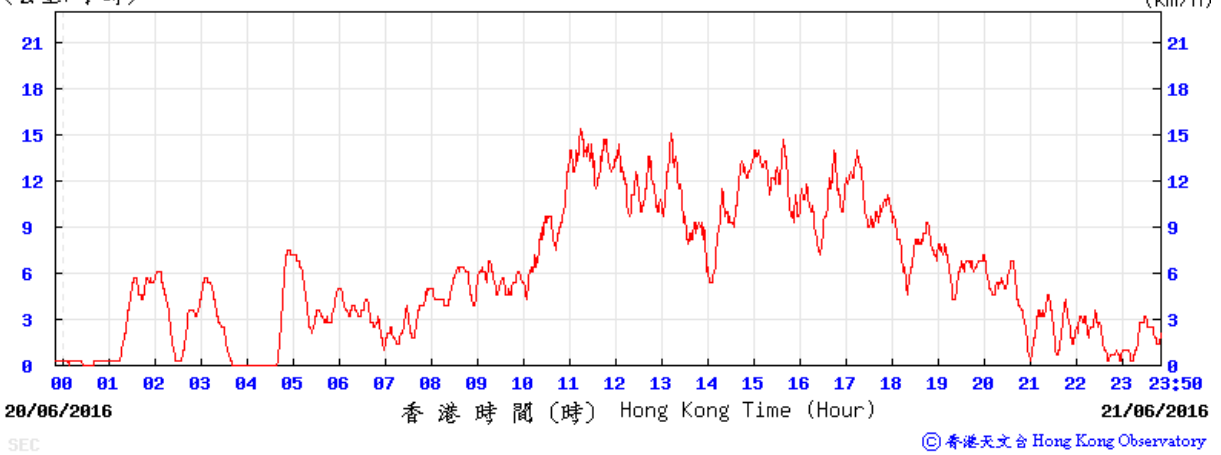
(公里/小時) (於香港時間 2016 年 6月21日23時50分更新) (Updated at 23:50H on 21 Jun 2016)



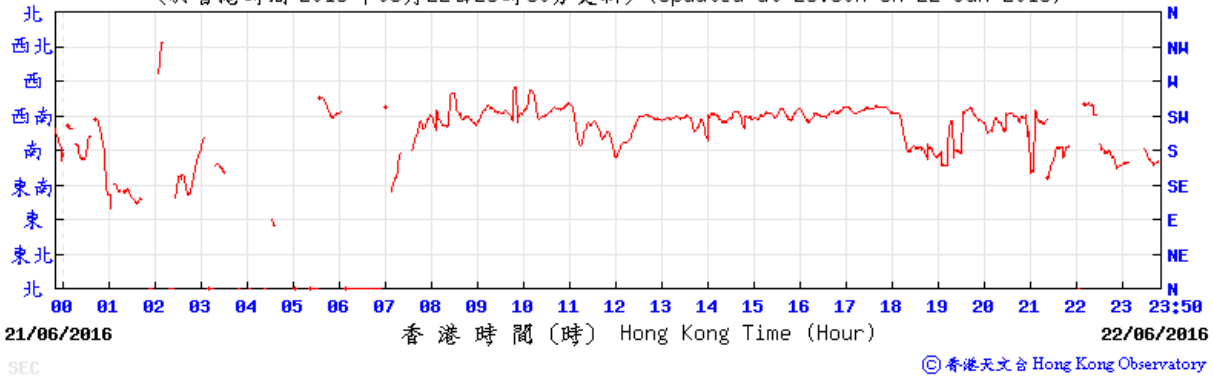(於香港時間 2016 年06月22日23時50分更新) (Updated at 23:50H on 22 Jun 2016)




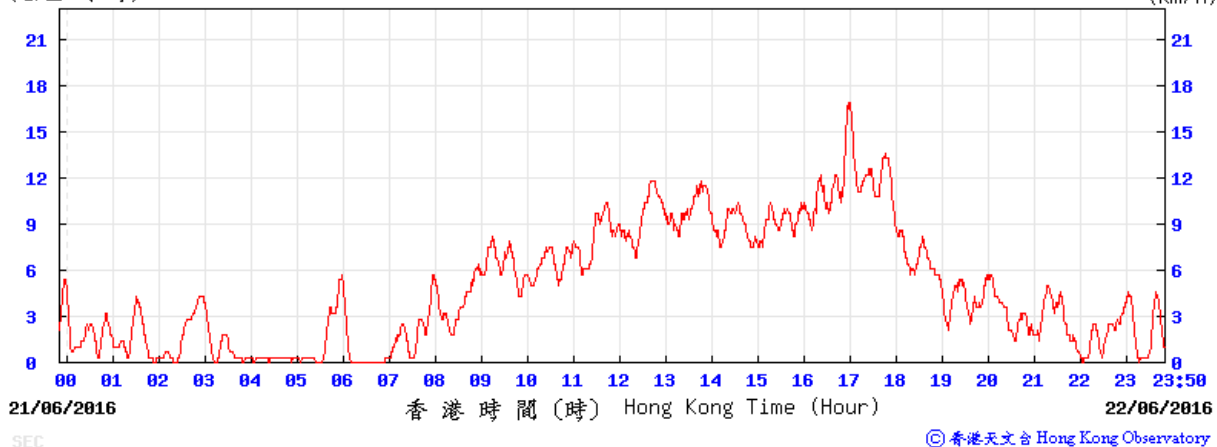(公里/小時) (於香港時間 2016 年 6月22日23時50分更新) (Updated at 23:50H on 22 Jun 2016) (km/h)






25 June 2016 – 26 June 2016

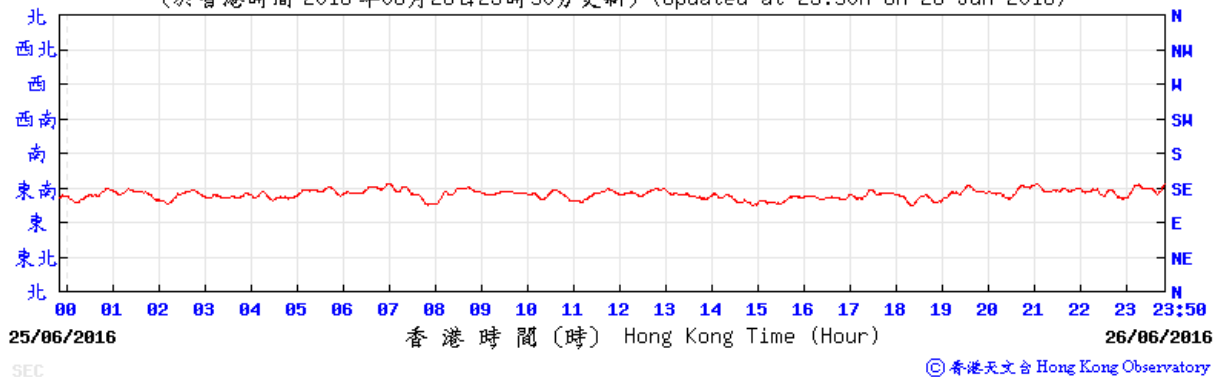(於香港時間 2016 年06月26日23時50分更新) (Updated at 23:50H on 26 Jun 2016)




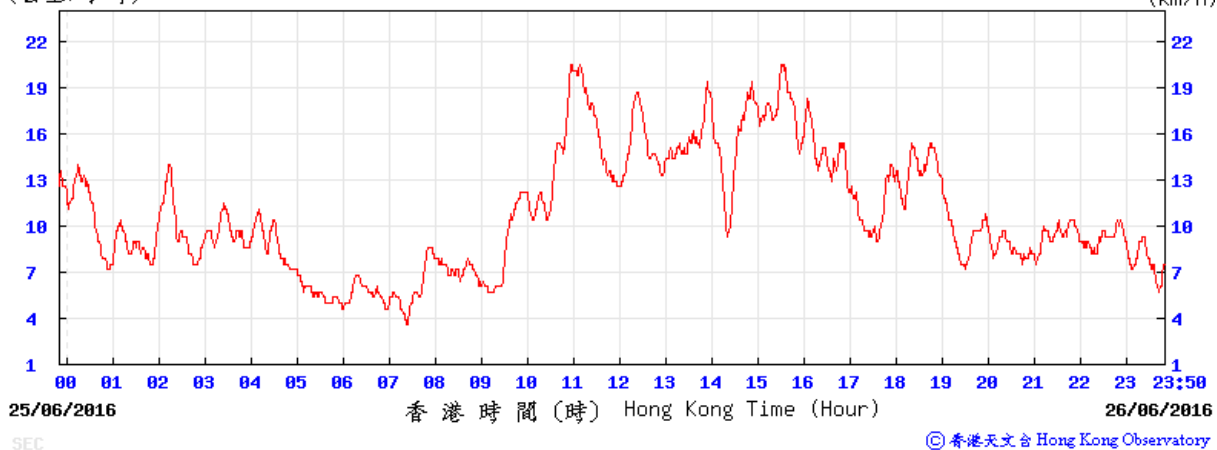
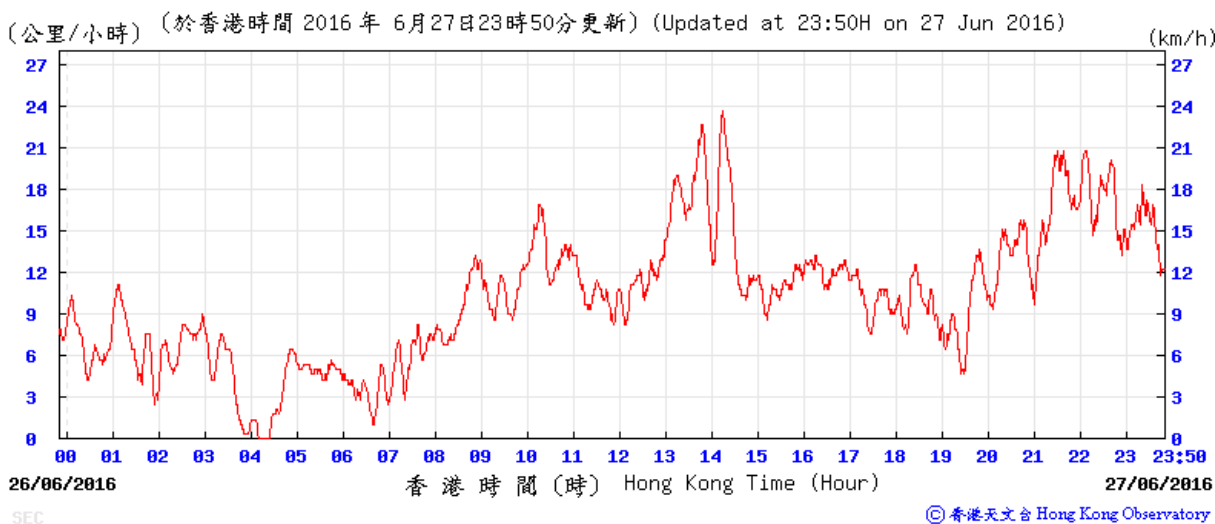
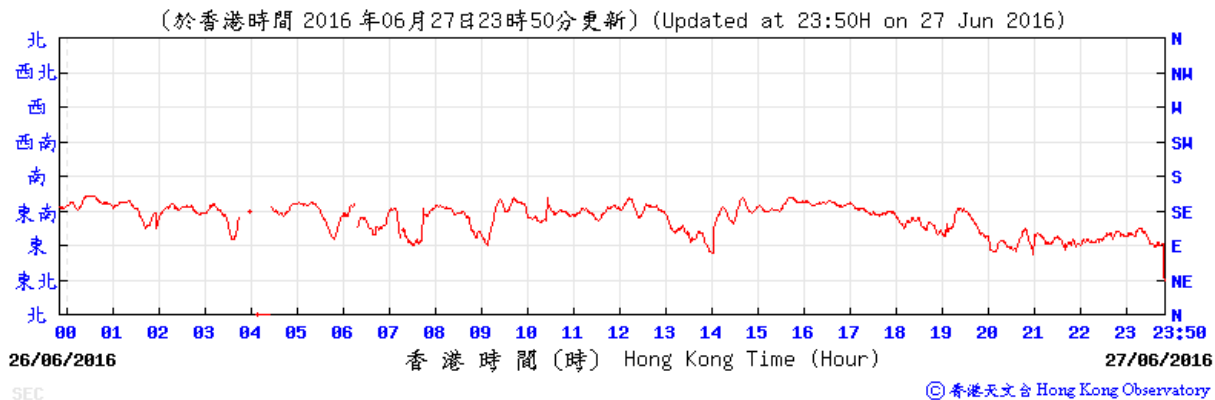
(公里/小時) (於香港時間 2016 年 6月26日23時50分更新) (Updated at 23:50H on 26 Jun 2016) (km/h)





30 June 2016 – 1 July 2016

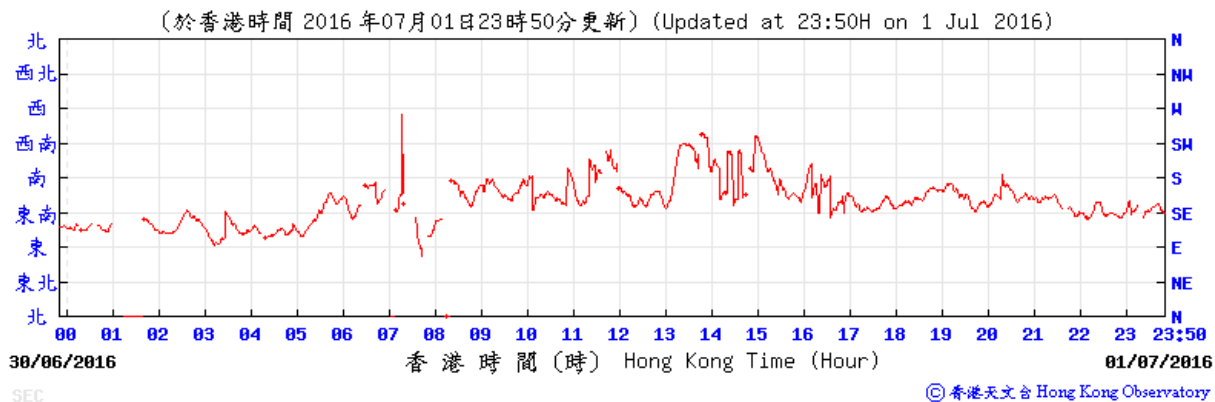

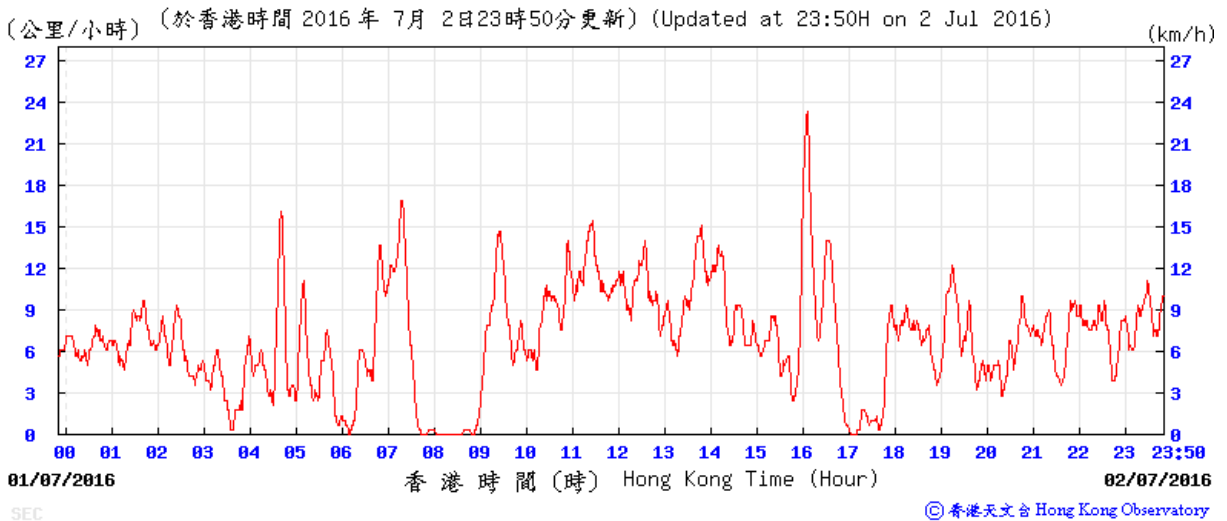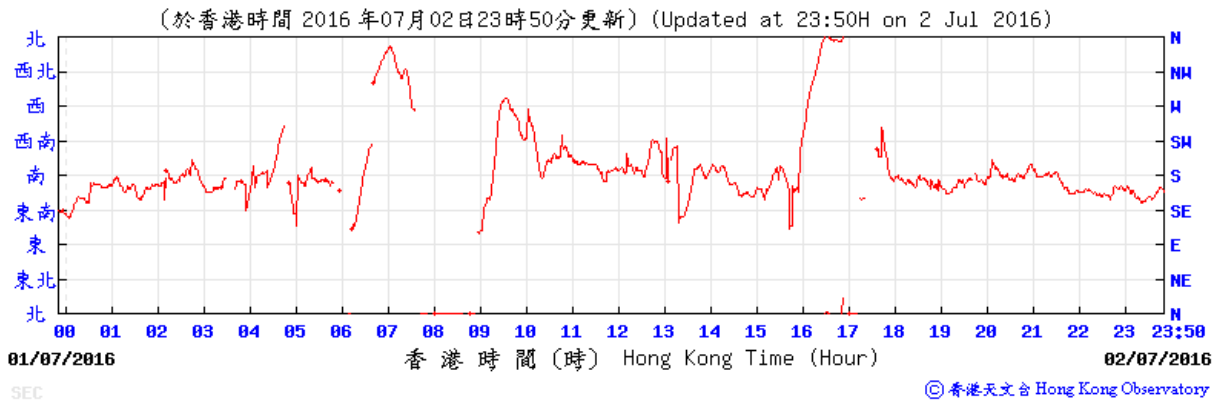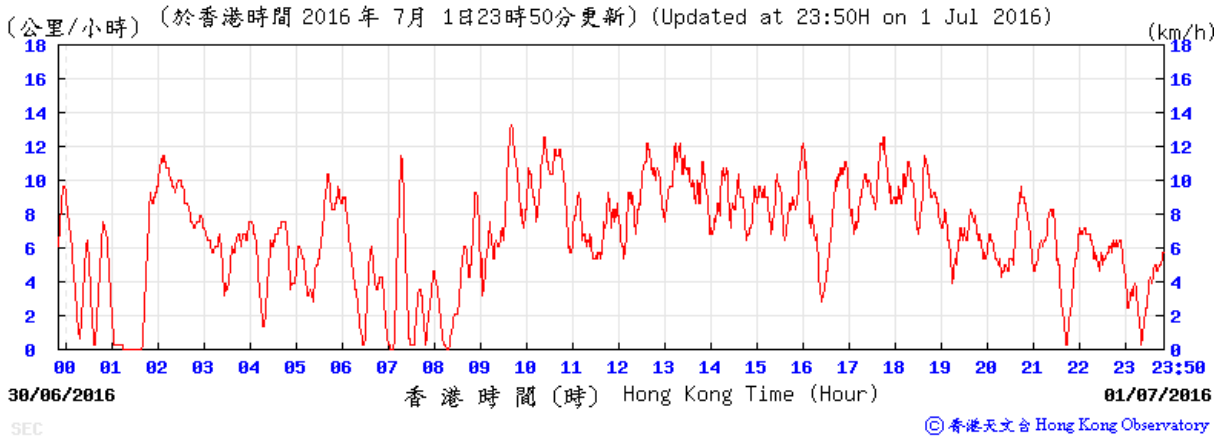

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,

Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars, one above and one below the text.

Appendix L

Cumulative statistics on Environmental Complaints, Notifications of Summons and Successful Prosecution

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
 Profit Industrial Building,
 1-15 Kwai Fung Crescent, Kwai Fong,
 Hong Kong..

Tel : (852)-24508238
 Fax : (852)-24508032
 Email : mcl@fugro.com.hk


Environmental Complaints Log

Complaint Log No.	Date of Receipt	Received From and Received By	Nature of Complaint	Date Investigated	Outcome	Date of Reply
Nil	-	-	-	-	-	-

Cumulative Statistics on Complaints

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Month	Cumulative Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

Cumulative Statistics on Notification of Summons and Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Notification of Summons and Prosecutions This Month	Cumulative Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,

Profit Industrial Building,

1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238

Fax : (852)-24508032

Email : mcl@fugro.com.hk

The logo for MaterialLab, featuring the word "MaterialLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars, one above and one below the text.

Appendix M

Summary of Site Audit in the Reporting Month

Summary of Site Audit in the Reporting Month

Parameters	Date	Observations and Recommendations	Follow-up
Air Quality	2 June 2016	Open stockpile shall be covered with impermeable sheeting to prevent dust emission at Portion Q.	The item was rectified by the Contractor and inspected on 8 June 2016.
	23 June 2016	Stock of more than 20 bags of cement or PFA should be covered entirely by impervious sheeting or placed in area sheltered on top and 3 sides at Portion N. Cement or PFA should be stored properly at Portion N.	The item was rectified by the Contractor and inspected on 30 June 2016.
Noise	NA		
Water Quality	23 June 2016	Stagnant water shall be removed at Portion Q.	The items were rectified by the Contractor and inspected on 30 June 2016.
	30 June 2016	Surface runoff shall be prevented from entering the discharge channel directly. Sediment in the channel shall be cleaned up at Portion P.	The items were rectified by the Contractor and inspected on 7 July 2016.
Chemical and Waste Management	8 June 2016	Chemicals and lubricant shall be stored properly at Portion M.	The items were rectified by the Contractor and inspected on 15 June 2016.
	15 June 2016	Construction waste shall be removed at Portion X.	The items were rectified by the Contractor and inspected on 23 June 2016.
	23 June 2016	Aluminum cans should be collected properly by separate labelled bins at Portion Q. Adequate recycling bins should be provided.	The items were rectified by the Contractor and inspected on 30 June 2016.
	30 June 2016	The hole of drip tray shall be sealed to prevent leakage of chemicals at all Zone.	The items were rectified by the Contractor and inspected on 7 July 2016.
Land Contamination	NA		
Landscape and Visual Impact	2 June 2016	Open stockpiles shall be covered by unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance at Portion Q..	The item was rectified by the Contractor and inspected on 8 June 2016.
General Condition	NA		

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab

Appendix N

Outstanding Issues and Deficiencies

MATERIALAB CONSULTANTS LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong..

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com.hk

MaterialLab**Summary of Outstanding Issues and Deficiencies in the Reporting Month**

Parameters	Outstanding Issues	Deficiencies
Air Quality	NA	Any items of deficiencies can be referred to Appendix M.
Noise	NA	
Water Quality	NA	
Chemical and Waste Management	NA	
Land Contamination	NA	
Landscape and Visual Impact	NA	
General Condition	NA	
Others	NA	
