

Our ref: 12-3-2021

12-3-2021

By hand

Environmental Protection Department  
Environmental Assessment Division  
Metro Assessment Group  
Kowloon Section (2)  
27th floor, Southorn Centre,  
130 Hennessy Road,  
Wan Chai, Hong Kong  
(Attn: Mr. TANG Ho Him, Matthew)

Dear Mr. TANG,

**Contract No. EDO 2/2020**  
**Environmental Monitoring Works for Contract No. ED/2018/05 – Kai Tak Development – Stage 5B Infrastructure Works at the Former North Apron Area**  
**Submission of Monthly EM&A Report for February 2021**

I refer to the Environment Permit (EP) No. EP-337/2009 and EP-445/2013/A for the captioned project.

Pursuant to Condition 3.3 of the EP-337/2009 and Condition of the 3.2 of the EP-445/2013/A, please find enclosed four hard copies and one electronic copy of Monthly EM&A Report for February 2021, which has been certified by the ET leader and verified by the IEC for your reference.

Thank you very much for your attention and please feel free to contact Mr. Lee at 2618 2166 should you require further information.

Yours faithfully,

For and on behalf of  
Ka Shing Management Consultant Limited

**AKCL**  
Applied knowledge center limited  
Company Secretary

Encl. Monthly EM&A report in February 2021

**Environmental Monitoring and Audit Report**  
**for**  
**Contract No. ED/2018/05 –**  
**Kai Tak Development – Stage 5B infrastructure**  
**works at the former north apron area**

**Contract No.: EDO 2/2020**

February 2021

(Version 1.1)

Certified By:  \_\_\_\_\_

(Environmental Team Leader)





**ACUITY**  
SUSTAINABILITY  
CONSULTING LIMITED



Website: [www.acuityhk.com](http://www.acuityhk.com)



Unit C, 11/F, Ford Glory Plaza,  
Nos. 37-39 Wing Hong Street,  
Cheung Sha Wan, Kowloon.



Tel. : (852) 2698 6833  
Fax.: (852) 2698 9383

Date: 12 March 2021  
Your ref:  
Our ref: PL-202103028

AECOM Asia Company Limited  
12/F, Grand Central Plaza, Tower 2,  
138 Shatin Rural Committee Road,  
Shatin, New Territories,  
Hong Kong

**Attn.: Mr. LEUNG Man Kit, CRE**

Dear Mr. Leung,

**Re: Agreement No. EDO 6/2019  
Independent Environmental Checker for Contract No. ED/2018/05 Kai Tak  
Development – Stage 5B Infrastructure works at the Former North Apron Area  
Verification of Monthly EM&A Report (February 2021)**

Reference is made to the Monthly EM&A Report (February 2021) provided by the Environmental Team on 12 March 2021.

Please be informed that we have no adverse comment on the captioned submission. We hereby verify the Monthly EM&A Report (February 2021) in accordance with Condition 3.3 of Environmental Permit No. EP-337/2009.

Thank you for your attention.

Yours sincerely,  
For and on behalf of  
Acuity Sustainability Consulting Limited

Kevin Li  
Independent Environmental Checker

c.c.	CEDD	Attn.: Mr. Kinox Wong	By email
	Ka Shing	Attn.: Mr. Chan Pang (ETL)	By email

**Table of Content**

**Page**

EXECUTIVE SUMMARY ..... 1

    Breaches of Action and Limit Levels ..... 1

    Complaint log ..... 1

    Notifications of summons and successful prosecutions ..... 2

    Report changes ..... 2

    Key construction works in the reporting month ..... 3

    Future key issues ..... 3

1.    INTRODUCTION..... 4

    Project Background ..... 4

    Project Organization ..... 5

    Works Area and Construction Programme ..... 5

    Construction works undertaken during reporting month..... 6

    Submission Status under the Environmental Permits ..... 6

2.    AIR QUALITY MONITORING ..... 7

    Monitoring Requirements ..... 7

    Monitoring Locations ..... 7

    Monitoring Parameters, Frequency and Duration ..... 7

    Monitoring Equipment ..... 8

    Monitoring Methodology and QA/QC Procedure ..... 8

    Wind Data Monitoring..... 11

    Action and Limit Levels ..... 11

    Impact Air Quality Monitoring results ..... 12

3.    NOISE MONITORING ..... 13

    Monitoring Requirements ..... 13

    Monitoring Locations ..... 13

    Monitoring Parameters, Frequency and Duration ..... 13

Monitoring Equipment .....	14
Monitoring Methodology and QA/QC Procedure .....	14
Maintenance and Calibration.....	15
Action and Limit Levels .....	15
Impact Noise Monitoring results .....	16
4. COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS .....	17
5. LANDSCAPE AND VISUAL MONITORING .....	19
Results and Observations.....	19
6. ENVIRONMENTAL SITE INSPECTION AND AUDIT .....	20
Site Inspection .....	20
Status of Waste Management .....	22
Status of Environmental Licenses, Notification and Permits .....	22
Implementation Status of Environmental Mitigation Measures.....	22
Environmental Complaint and Non-compliance .....	23
Notifications of summons and successful prosecutions .....	23
7. FUTURE KEY ISSUES .....	25
Construction Programme in the coming month.....	25
Environmental Site Inspection and Monitoring Schedule for next month .....	26
8. CONCLUSIONS .....	27

**List of Tables**

Table I	Non-compliance Record in the Reporting Month
Table II	Summary of complaints in the Reporting Month
Table III	Summary of summons and successful prosecutions in the Reporting Month
Table IV	Summary of future key issues and potential impact in the coming month
Table 1.1	Contact Information of Key Personnel
Table 1.2	Major activities of the Project during reporting month
Table 1.3	Summary of Status of Required Submission of EPs

Table 2.1	Locations of Air Quality Monitoring Stations
Table 2.2	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.3	Air Quality Monitoring Equipment
Table 2.4	Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring
Table 2.5	Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring
Table 2.6	Summary of 24-hour average TSP Monitoring Data during the reporting month
Table 2.7	Summary of 1-hour average TSP Monitoring Data during the reporting month
Table 3.1	Locations of Noise Monitoring Stations
Table 3.2	Noise Monitoring Parameters, Frequency and Duration
Table 3.3	Noise Monitoring Equipment
Table 3.4	Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring
Table 3.5	Summary of Noise Monitoring Data during the reporting month
Table 4.1	Comparison of 24-hour average TSP Monitoring Data with EIA predictions
Table 4.2	Comparison of 1-hour average TSP Monitoring Data with EIA predictions
Table 4.3	Comparison of Noise Monitoring Data with EIA predictions
Table 5.1	Summary of observations of Landscape and Visual impact during the reporting month
Table 6.1	Summary of site inspections observations during the reporting month
Table 6.2	Summary of Environmental Licenses, Notifications and Permits
Table 6.3	Summary of complaints in the Reporting Month
Table 6.4	Summary of summons and successful prosecutions in the Reporting Month
Table 7.1	Summary of future key issues and potential impact in the coming month

### **List of Figure**

Figure 1 – Proposed works of Contract No. ED/2018/05

Figure 2 – Proposed works of Contract No. ED/2018/05

Figure 3 – D1 Road Site Layout Plan

Figure 4 – Site Layout Plan

Figure 5 – Air Quality Monitoring Stations

Figure 6 – Noise Monitoring Stations

### **List of Appendices**

Appendix A – Organization Chart of EM&A Team

Appendix B – Construction Programme

Appendix C – Environmental monitoring schedules

Appendix D – Photographic records

Appendix E – Calibration certificates, catalogue of air quality monitoring equipment

Appendix F – Weather information

Appendix G – 24-hr TSP monitoring results and graphical presentation

Appendix H – 1-hr TSP monitoring results and graphical presentation

Appendix I – Event and Action Plan for air quality

Appendix J – Calibration certificates, catalogue of noise monitoring equipment

Appendix K – Noise monitoring results and graphical presentation

Appendix L – Event and Action Plan for noise

Appendix M – Event and Action Plan for Landscape and Visual Impact

Appendix N – Waste Flow Table

Appendix O – Environmental Mitigation Implementation Schedule (EMIS)

Appendix P – Summaries of Environmental Complaint, Warning, Summon and Notification of  
Successful Prosecution

## EXECUTIVE SUMMARY

1. This is the 1<sup>st</sup> Monthly Environmental Monitoring & Audit (EM&A) report which summaries the findings of the EM&A Programme during the reporting period from 16 to 28 February 2021.

### **Breaches of Action and Limit Levels**

2. 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
3. 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
4. Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
5. Summary of the non-compliance in the reporting month for the Project is tabulated in Table I.

*Table I Non-compliance Record in the Reporting Month*

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
1-hr TSP	0	0	N/A
24-hr TSP	0	0	N/A
Construction noise	0	0	N/A

### **Complaint log**

6. No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table II.

*Table II Summary of complaints in the Reporting Month*

Date of Notification from EPD	Date of compliant	Description of complaint	Recommendations / Action take	Close-out date / Status
No complaint	NA	NA	NA	NA

Date of Notification from EPD	Date of compliant	Description of complaint	Recommendations / Action take	Close-out date / Status
was received in the reporting month.				

**Notifications of summons and successful prosecutions**

7. No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table III.

*Table III Summary of summons and successful prosecutions in the Reporting Month*

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
No notification of summons and successful prosecutions were received in the reporting month.	NA	NA	NA	NA

**Report changes**

8. There was no reporting change in the reporting month.

### **Key construction works in the reporting month**

9. Major construction activities undertaken during the reporting month included:

- Construction of site hoarding
- Construction of publicity board
- Construction of box culvert
- Pre-drilling works
- Bored pile works for landscape elevated walkway
- Demolition of existing structure and cottage

### **Future key issues**

10. The future key issues and potential impact in the coming month are given in Table IV.

*Table IV Summary of future key issues and potential impact in the coming month*

Future key issues in the coming month	Potential impact
Construction of box culvert	Noise and Air Quality
Pre-drilling works	Noise and Air Quality
Bored pile works for landscape elevated walkway	Noise and Air Quality
Demolition of existing structure and cottage	Noise and Air Quality
Construction of underground works at pedestrian streets	Noise and Air Quality



# 1. INTRODUCTION

## **Project Background**

- 1.1 The Kai Tak Development (KTD) is located in the southern part of Kowloon Peninsula of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling.
- 1.2 Contract No. ED/2018/05 - Kai Tak Development – stage 5B infrastructure works at the former north apron area (The Project), comprises mainly the design and construction of a section of dual two-lane Road D1; single two-lane Road L9 and Road L16; a single-lane slip road S14; a pedestrian subway SB-01; an elevated walkway LW-02; renovation of the existing pedestrian subways KS9, KS10 and KS32, as well as modification of the southern end of the existing pedestrian subway KS10; associated footpaths, street lighting, traffic aids, drainage, sewerage, water mains, landscaping, electrical and mechanical works, and ancillary works. The proposed works are shown in Figure 1 and Figure 2. The proposed works and site boundary are shown in Figure 3 and Figure 4. Civil Engineering and Development Department (CEDD) had completed an Environmental Impact Assessment (EIA) and is the Permit Holder.
- 1.3 In accordance with the approved EIA Reports, Environmental Monitoring and Audit (EM&A) programmes are recommended to ensure compliance with the EIA study recommendations. The project proponent was the Civil Engineering and Development Department (CEDD). AECOM Asia Co. Ltd. (AECOM) was commissioned by CEDD as Supervisor (act as Engineers' Representative (ER) listed in EM&A Manual). Acuity Sustainability Consulting Limited (Acuity) was commissioned as the Independent Environmental Checker (IEC). Build King – STEC Joint Venture (Build King) was appointed as the main Contractor for the construction works of Contract No. ED/2018/05. Ka Shing was commissioned by CEDD to undertake the role of the Environmental Team (ET) to implement the EM&A programme for The Project.
- 1.4 The construction work under ED/2018/05 comprises the EM&A Manual (EIA Register No. AEIAR-130/2009 for Kai Tak Development) and Environmental Permit No. EP- 337/2009.
- 1.5 Air quality and noise monitoring has been proposed in the EM&A Manual with EIA Register No. AEIAR-130/2009 for Kai Tak Development.

## **Project Organization**

1.6 The project organization chart and with respect to the EM&A programme is shown in Appendix A. Information of key personnel contact names and telephone numbers are summarized in Table 1.1.

*Table 1.1 Contact Information of Key Personnel*

Party	Role	Contact Person	Position	Phone No.	Fax No.
Civil Engineering and Development Department (CEDD)	Project Proponent	Mr. George Ng	Senior Engineer	3842 7107	3842 7107
		Mr. Kinox Wong	Engineer	3842 7137	3842 7137
AECOM Asia Co. Ltd. (AECOM)	Supervisor (act as Engineers' Representative (ER) listed in EM&A Manual)	Mr. Leung Wai Kit	CRE	2412 3410	2798 0783
Acuity Sustainability Consulting Limited (Acuity)	Independent Environmental Checker (IEC)	Mr. Kevin Li	IEC	2698 6833	2698 9383
Ka Shing Management Consultant Limited (Ka Shing)	Environmental Team (ET)	Ir. Chan Pang	ET Leader	2618 2166	2120 7752
Build King – STEC Joint Venture (BK-STECC)	Contractor	Mr. Raymond Lam	Environmental Officer	9713 6817	3850 8508

## **Works Area and Construction Programme**

1.7 The construction works commenced on 16 February 2021. The construction programme of the Project is given in Appendix B.

### **Construction works undertaken during reporting month**

1.8 Major construction works of the Project in the reporting month are summarized in Table 1.2:

*Table 1.2 Major activities of the Project during reporting month*

Construction of site hoarding	Construction of publicity board
Construction of box culvert	Pre-drilling works
Bored pile works for landscape elevated walkway	Demolition of existing structure and cottage

### **Submission Status under the Environmental Permits**

1.9 The status of required submission under Environmental Permit (EP) conditions under EP-337/2009 are summarized in Table 1.3.

*Table 1.3 Summary of Status of Required Submission of EPs*

EP Condition EP-337/2009	Submission	Submission Date
Condition 1.11	Notification of Commencement Date of Construction of the Project	12 Jan 2021
Condition 2.3	Management Organization of Main Construction Companies	21 Sep 2020
Condition 2.4	Design Drawings	12 Jan 2021
Condition 2.11	Landscape Mitigation Plans	17 Dec 2020
Condition 3.2	Baseline Monitoring Report	12 Jan 2021

## 2. AIR QUALITY MONITORING

### Monitoring Requirements

2.1 In accordance with the EM&A Manual with EIA Register No. AEIAR-130/2009, baseline monitoring shall be carried out at all of the designated monitoring locations for at least 14 consecutive days prior to the commissioning of the construction works to obtain daily 24-hour TSP samples. 1-hour TSP sampling shall also be done at least 3 times per day prior to the commencement of the construction works.

### Monitoring Locations

2.2 Two designated monitoring stations were selected for air quality monitoring programme. Impact air quality monitoring was conducted at three air quality monitoring stations in the reporting month. Table 2.1 describes the air quality monitoring locations, which are also depicted in Figure 5.

*Table 2.1 Locations of Air Quality Monitoring Stations*

Air Quality Monitoring Locations for the Project	Location of Measurement
AM2(A) – Ng Wah Catholic Secondary School	Rooftop
AM3 – Sky Tower	Podium floor near T7

### Monitoring Parameters, Frequency and Duration

2.3 The air quality monitoring locations and monitoring frequency are listed in Table 2.2.

*Table 2.2 Air Quality Monitoring Parameters, Frequency and Duration*

Air Monitoring Station	Location for Measurement	Parameter	Duration	Frequency
AM2(A) – Ng Wah Catholic Secondary School	Rooftop	- 24-hour average TSP	- 24 hours	- Once every 6 days
AM3 – Sky Tower	Podium Floor near Tower 7	- 1-hour average TSP	- 1 hour	- Three times every 6 days

2.4 The monitoring schedule for reporting month and next month is presented in Appendix C.

2.5 Photographic records of the impact monitoring setup are shown in Appendix D.

### **Monitoring Equipment**

2.6 24-hour average TSP and 1-hour average TSP levels were measured for impact monitoring. 24-hour average TSP levels were measured by the High Volume Samplers (HVS) and 1-hour average TSP levels were measured by direct reading method to indicate short-term impacts. Wind data monitoring equipment was set up at conspicuous locations for logging wind speed and wind direction near to the dust monitoring locations. Table 2.3 summarizes the equipment to be used in the air quality monitoring.

*Table 2.3 Air Quality Monitoring Equipment*

Equipment	Model	Quantity	Calibration Interval
HVS Sampler	TE-5170 X c/w of TSP sampling inlet	2	2 months
HVS Calibrator	TISCH TE-5025A	1	1 year
1-hour TSP Dust Meter	TSI Model AM510 SidePak Personal Aerosol Monitor	2	1 year
Wind Logger	Wind Logger with Pro-D sensor	1	6 months

2.7 High volume samplers (HVS) (TE-5170 X c/w of TSP sampling inlet) comprising with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

2.8 Calibration certificates, catalogue of equipment are given in Appendix E.

### **Monitoring Methodology and QA/QC Procedure**

#### ***24-hour TSP Monitoring***

#### **Operating/Analytical Procedures**

2.9 Setup criteria of HVS are shown as follows:

- A horizontal platform with appropriate support to secure the samplers against gusty wind was provided.
- No two samplers were placed less than 2m apart.
- The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2m of separation from walls, parapets and penthouses was set for the rooftop samples.
- A minimum of 2m separation from any supporting structure, measured horizontally was set.
- No furnaces or incineration flues was nearby.
- Airflow around the sampler was unrestricted.
- The sampler was more than 20m from the dripline.
- Any wire fence and gate, to protect the samplers, was not caused any obstruction during monitoring.
- Permission were obtained to setup the samplers and to obtain access to the monitoring stations.
- A secured supply of electricity was provided to operate the samplers.

2.10 Prior to the commencement of the dust sampling, the flow rate of the HVS was properly set (between 1.1 m<sup>3</sup>/min. and 1.7 m<sup>3</sup>/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.

2.11 For TSP sampling, Glass Fiber Filter Media 8" x 10" having a collection efficiency of > 99 % for particles of 0.3 µm diameter were used.

2.12 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.

2.13 The filter holding frame was removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.

2.14 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure was sufficient to avoid air leakage at the edges.

2.15 The shelter lid was closed and secured with the aluminium strip.

2.16 The timer was programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).

2.17 After sampling, the filter was removed from the HVS and put into a clean and labeled seal plastic bag to avoid cross contamination. The elapsed time was also be recorded. The sampled filters were sent to the Castco Testing Centre Limited for weighting.

2.18 Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature was between 25°C and 30°C and not vary by more than  $\pm 3^\circ\text{C}$ ; the relative humidity (RH) was less than 50% and not vary by more than  $\pm 5\%$ . A convenient working RH is 40%.

### Maintenance/Calibration

2.19 The following maintenance/calibration are required for the HVS:

- The HVS and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
- High volume samplers were calibrated with at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

### ***1-hour TSP Monitoring***

### Measurement Procedures

2.20 The measurement procedures of the 1-hour TSP were conducted in accordance with the Manufacturer's Instruction Manual as follows:

- Set up the dust meter on a tripod at 1.2m level.
- Turned on the dust meter and check the battery, if too low, change new ones. Pointed the meter to the source area or the planned measurement area.
- The zero calibration of the instrument was conducted before and after each sampling.
- TSP levels were recorded for 1-hour with 5-minute data logging interval.
- Recorded down the general meteorological conditions, Test ID no., start/end time, spot check reading at each sampling location for data processing.
- Recorded any activities that may generate dust during measurement period.

## Maintenance/Calibration

2.21 The following maintenance/calibration are required for the direct dust meters:

- To validate the accuracy of dust meter, compare the results measured by dust meter and HVS every 12 months throughout all stages of the air quality monitoring.

## Wind Data Monitoring

2.22 Wind Anemometer was installed at the roof-top of AM2(A) – Ng Wah Catholic Secondary School with 10m above ground and clear of constructions or turbulence caused by the buildings.

2.23 The wind data was captured by a data logger and the data was downloaded at least once per month for analysis.

2.24 The wind data monitoring equipment will be re-calibrated at least once every six months.

2.25 Wind direction is divided into 16 sectors of 22.5 degrees each.

2.26 Details of weather information during the monitoring period are shown in Appendix F.

## Action and Limit Levels

2.27 The Action and Limit Levels of 24-hour average TSP and 1-hour average TSP are summarized in Table 2.4 and Table 2.5 respectively.

*Table 2.4 Action and Limit Levels of 24-hour average TSP for Construction Dust Monitoring*

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
24-hour average TSP	AM2(A)	175	260
	AM3	172	260

*Table 2.5 Action and Limit Levels of 1-hour average TSP for Construction Dust Monitoring*

Parameter	Air Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hour average TSP	AM2(A)	302	500
	AM3	301	500



## **Impact Air Quality Monitoring results**

2.28 Impact monitoring results for 24-hour average TSP and 1-hour average TSP levels at the designed air quality monitoring stations are summarized in Table 2.6 and Table 2.7 respectively.

*Table 2.6 Summary of 24-hour average TSP Monitoring Data during the reporting month*

Air Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM2(A)	83	62-103	175	260
AM3	78	57-98	172	260

*Table 2.7 Summary of 1-hour average TSP Monitoring Data during the reporting month*

Air Monitoring Station	Average TSP Concentration, $\mu\text{g}/\text{m}^3$	Range, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM2(A)	50	47-53	302	500
AM3	37	33-42	301	500

2.29 There was no Action and Limit Level exceedance of 24-hour average TSP and 1-hour average TSP levels recorded during the reporting month.

2.30 Graphical presentation and detailed monitoring results of 24-hour average TSP and 1-hour average TSP levels are shown in Appendix G and Appendix H respectively.

2.31 The Event and Action Plan is provided in Appendix I.

2.32 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

2.33 Weather conditions during the monitoring periods were generally fine and did not affect the monitoring results.

### 3. NOISE MONITORING

#### Monitoring Requirements

- 3.1 In accordance with EM&A Manuals (EIA Register No. AEIAR-130/2009), impact noise monitoring shall be carried out during the construction phase of the Project.
- 3.2 Regular monitoring,  $L_{Aeq, 30\text{-minute}}$ , for each station will be on a weekly basis and conduct one set of measurements between 0700 – 1900 on normal weekdays.
- 3.3 If construction works are extended to include works during 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring will be carried out during the respective restricted hours periods.

#### Monitoring Locations

- 3.4 Two designated monitoring stations were selected for noise monitoring programme. Impact noise monitoring was conducted at two noise monitoring stations in the reporting month. Table 3.1 describes the noise monitoring locations, which are also depicted in Figure 6.

*Table 3.1 Locations of Noise Monitoring Stations*

Noise Monitoring Locations for the Project	Location of Measurement
M4(A) – Le Billionnaire	Podium (Façade)
M5(A) – Prince Ritz	Podium (Façade)

#### Monitoring Parameters, Frequency and Duration

- 3.5 The noise monitoring locations and monitoring frequency are listed in Table 3.2.

*Table 3.2 Noise Monitoring Parameters, Frequency and Duration*

Noise Monitoring Station	Location for Measurement	Parameter	Frequency and Duration
M4(A) – Le Billionnaire	Podium (Façade)	L <sub>Aeq</sub> , L <sub>A10</sub> and L <sub>A90</sub>	30 - minutes measurement at each monitoring station between 0700 – 1900 hrs on normal weekdays (Monday to Saturday) at frequency of once per week.
M5(A) – Prince Ritz	Podium (Façade)		

3.6 The monitoring schedule for reporting month and next month is presented in Appendix C.

3.7 Photographic records of the monitoring setup are shown in Appendix D.

### **Monitoring Equipment**

3.8 As referred to the Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO), sound level meters in compliance with the IEC 61672-1 (Type 1) standard [this standard replaced the International Electrotechnical Commission Publications 60651:1979 (Type 1) and 60804:1985 (Type 1)] were used for noise monitoring. Table 3.3 summarizes the equipment to be used in the noise monitoring.

*Table 3.3 Noise Monitoring Equipment*

Equipment	Model	Quantity	Calibration Interval
Sound Level Meter	RION NL52	1	1 year
Sound Level Calibrator	RION NC 74	1	1 year
Air Flowmeter	TSI TA440 Air Velocity	2	1 year

3.9 Calibration certificates, catalogue of equipment are given in Appendix J.

### **Monitoring Methodology and QA/QC Procedure**

3.10 The noise level measurement was conducted at 1m from the exterior of the nearby noise sensitive receivers building façade and at 1.2m above the ground and facing to the source area or the planned measurement area.

3.11 No noise measurement was conducted in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. Air flow was measured by air flow meter.

3.12 Turned on the sound level meter and check the battery, if too low, change new ones.

3.13 Calibration was conducted immediately prior to and after each noise measurement, the accuracy of the sound level meters was checked by using sound calibrator generating 1,000 Hz with 94dB. Measurement data was found to be valid only if the calibration levels from before and after the noise measurement agreed to within 1.0 dB.

3.14 Noise level was recorded.

3.15 Recorded any activities that may generate noise during measurement period.

### **Maintenance and Calibration**

3.16 The microphone of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.

3.17 The sound level meter and sound calibrator were calibrated annually.

3.18 Calibration for sound level meter was conducted immediately prior to and following each noise measurement by using sound calibrator generating a known sound pressure level at a known frequency (1,000 Hz with 94dB). Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

### **Action and Limit Levels**

3.19 The Baseline Noise Levels and Action and Limit Levels for construction noise is presented in Table 3.4.

*Table 3.4 Baseline Noise Level and Action and Limit Levels for Construction Noise Monitoring*

Time Period	Noise Monitoring Station	Baseline Noise Levels, dB (A)	Action Level	Limit Level <sup>^</sup>
0700 – 1900 on normal weekdays	M4(A)	69.5	When one documented complaint is received.	75 dB(A)
	M5(A)	72.5		

Note: ^ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

**Impact Noise Monitoring results**

3.20 Impact noise monitoring results at the designed noise monitoring stations are summarized in Table 3.5 respectively.

*Table 3.5 Summary of Noise Monitoring Data during the reporting month*

Noise Monitoring Station	Measured $L_{Aeq, 30-min}$ , Average, dB(A)	Measured $L_{Aeq, 30-min}$ , Range, dB(A)	Action Level	Limit Level <sup>^</sup>
M4(A)	69.1	69.0 – 69.2	When one documented complaint is received	75 dB(A)
M5(A)	71.9	70.9 – 73.2		

Note: ^ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

3.21 There was no Action and Limit Level exceedance of  $L_{Aeq, 30-min}$  recorded during the reporting month.

3.22 Graphical presentation and detailed monitoring results are shown in Appendix K.

3.23 The Event and Action Plan is provided in Appendix L.

3.24 Non-project related construction activities in the adjacent construction sites were observed during the reporting period and may affect the monitoring results.

3.25 Weather conditions during the monitoring periods were generally fine and did not affect the monitoring results.

## 4. COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS

4.1 The environmental impacts predictions were given in Agreement No. CE 35/2006(CE) Kai Tak Development Engineering Study cum Design and Construction of Advance Works - Investigation, Design and Construction - Kai Tak Development Environmental Impact Assessment Report, EIA Register No. AEIAR-130/2009 for Kai Tak Development (The EIA Report). The EM&A data was compared with the EIA predictions as summarized in Table 4.1 to Table 4.3.

*Table 4.1 Comparison of 24-hour average TSP Monitoring Data with EIA predictions*

Air Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 24-hour average TSP concentration		Measured 24-hr average TSP in Reporting Month (February 2021) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM2(A) - Ng Wah Catholic Secondary School	NA	NA	NA	62 – 103
AM3 - Sky Tower	A40 <sup>^</sup>	106	138	57 – 98

Note:

<sup>^</sup> Prediction results are given in the Table 3.13 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

*Table 4.2 Comparison of 1-hour average TSP Monitoring Data with EIA predictions*

Air Monitoring Station	ASR No. in EIA report	Predicted Cumulative Maximum 1-hour average TSP concentration		Measured 1-hr average TSP in Reporting Month (February 2021) $\mu\text{g}/\text{m}^3$
		Scenario 1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario 2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	
AM2(A) - Ng Wah Catholic Secondary School	NA	NA	NA	47 – 53
AM3 - Sky Tower	A40	217 <sup>^</sup>	247 <sup>^</sup>	33 – 42

Note:

<sup>^</sup> Prediction results are given in the Table 3.13 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

*Table 4.3 Comparison of Noise Monitoring Data with EIA predictions*

Noise Monitoring Station	NSR No. in EIA report	Predicted Mitigated Construction Noise Levels during Normal Daytime Working Hour $L_{Aeq, 30min}$ , dB(A)	Measured Noise Level in Reporting Month (February 2021) $L_{Aeq, 30min}$ , dB(A)
M4(A) – Le Billionnaire	NA	NA	69.0 – 69.2

Noise Monitoring Station	NSR No. in EIA report	Predicted Mitigated Construction Noise Levels during Normal Daytime Working Hour $L_{Aeq, 30min}$ , dB(A)	Measured Noise Level in Reporting Month (February 2021) $L_{Aeq, 30min}$ , dB(A)
M5(A) – Prince Ritz	NA	NA	70.0 – 73.2

Note:

\* Prediction results are given in the Table 3.20 of the EIA report EIA Register Nos. AEIAR-130/2009 for Kai Tak Development.

- 4.2 No prediction in the EIA Report for 24-hour TSP monitoring results at AM2(A).
- 4.3 24-hour TSP monitoring results at AM3 was recorded lower than the prediction in the EIA Report.
- 4.4 No prediction in the EIA Report for 1-hour TSP monitoring results at AM2(A).
- 4.5 1-hour TSP monitoring results at AM3 was recorded lower than the prediction in the EIA Report.
- 4.6 No prediction in the EIA Report for noise monitoring results at M4(A) and M5(A).

## 5. LANDSCAPE AND VISUAL MONITORING

5.1 In accordance with EM&A Manual (EIA Register No. AEIAR-130/2009), Landscape and Visual Monitoring shall be carried out during the construction phase of the Project. Regular impact monitoring will be conducted at least once per week.

### Results and Observations

5.2 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.

5.3 Site inspections were conducted on 4 Feb, 11 Feb, 18 Feb and 25 Feb 2021 in the reporting month.

5.4 The summary of site audits is attached in Table 5.1.

*Table 5.1 Summary of observations of Landscape and Visual impact during the reporting month*

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
4 Feb 2021	No	NA	NA
11 Feb 2021	No	NA	NA
18 Feb 2021	No	NA	NA
25 Feb 2021	No	NA	NA

5.5 No non-compliance of the landscape and visual impact was recorded in the reporting month.

5.6 Should non-compliance of the landscape and visual impact occur, action in accordance with the action plan presented in Appendix M shall be performed.











## 6. ENVIRONMENTAL SITE INSPECTION AND AUDIT

### Site Inspection

- 6.1 Site inspections were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 6.2 Site inspections were conducted on 4 Feb, 11 Feb, 18 Feb and 25 Feb 2021 in the reporting month.
- 6.3 The summaries of site audits is attached in Table 6.1.

*Table 6.1 Summary of site inspections observations during the reporting month*

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
4 February 2021	 <p>Observation: Styrofoam lunch box was found near skip at B1.</p>	 <p>Action Taken: Styrofoam lunch box and waste was removed.</p>	Closed out 11 Feb 2021
4 February 2021	 <p>Observation: Waste stored in the container should be cleared regularly.</p>	 <p>Action Taken: Waste in the container was cleared.</p>	Closed out 11 Feb 2021

Inspection Date	Key Observations	Recommendations / Actions	Close-out Date / Status
11 February 2021	 <p>Observation: The stockpile was not covered.</p>	 <p>Action Taken: The stockpile was covered.</p>	Closed out 18 February 2021
18 February 2021	 <p>Observation: Waste was found in the skip at B1.</p>	 <p>Action Taken: Waste in the skip was cleared.</p>	Closed out 25 February 2021
25 February 2021	 <p>Observation: Ensure the discharge pipeline to rainwater drain was properly connected to sedimentation tank or wastewater discharge system.</p>	 <p>Action Taken: Discharge pipeline was connected to sedimentation tank properly.</p>	Closed out 4 Mar 2021
25 February 2021	 <p>Observation: The drip tray of gen-set should be plugged to prevent any leakage.</p>	 <p>Action Taken: The dip tray of get-set was plugged to prevent any leakage.</p>	Closed out 4 Mar 2021

## **Status of Waste Management**

- 6.4 The amount of wastes generated by the major site activities of the work contracts within the Project during the reporting month is shown in Appendix N.
- 6.5 The Contractor was registered as a chemical waste producer for the Project. The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

## **Status of Environmental Licenses, Notification and Permits**

- 6.6 A summary of the relevant permits, licenses and/or notifications on environmental protection for the Project is shown in Table 6.2.

*Table 6.2 Summary of Environmental Licenses, Notifications and Permits*

Environmental Licenses, Notifications and Permits	Ref. No.	Valid Form	Valid Till
Environmental Permit under EIAO	EP-337/2009	23 Apr 2009	N/A
Construction Dust Notification under APCO	HA/1826/1	29 Dec 2020	N/A
Waste Disposal Billing Account	7038086	21 Aug 2020	N/A
Registration as a Chemical Waste Producer	511-286-B2596-01	15 Sep 2020	N/A
Wastewater Discharge License under WPCO	Application in progress	NA	NA
Construction Noise Permit	Application in progress	NA	NA

## **Implementation Status of Environmental Mitigation Measures**

- 6.7 The Contractor has implemented environmental mitigation measures and requires as stated in the EIA reports, the EP and the EM&A Manuals. The implementation status of the mitigation

measures is summarized in Appendix O.

**Environmental Complaint and Non-compliance**

6.8 No complaint was received in the reporting month. Summary of complaints in the reporting month is tabulated in Table 6.3.

*Table 6.3 Summary of complaints in the Reporting Month*

Date of Notification from EPD	Date of compliant	Description of complaint	Recommendations / Action taken	Close-out date / Status
No complaint was received in the reporting month.	NA	NA	NA	NA

6.9 Complaint log is shown in Appendix P.

**Notifications of summons and successful prosecutions**

6.10 No notification of summons and successful prosecutions was received in the reporting month. Summary of summons and successful prosecutions in the reporting month is tabulated in Table 6.4.

*Table 6.4 Summary of summons and successful prosecutions in the Reporting Month*

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
No notification of summons and successful prosecutions were	NA	NA	NA	NA

Date of receiving notification of summons or prosecutions	Date of event	Description of event	Action taken	Close-out date / Status
received in the reporting month.				

6.11 The summaries of cumulative environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in Appendix P.

## 7. FUTURE KEY ISSUES

### Construction Programme in the coming month

7.1 The major construction activities and potential impacts in the next reporting month as follows:

*Table 7.1 Summary of future key issues and potential impact in the coming month*

Future key issues in the coming month	Potential impact
Construction of box culvert	Noise and Air Quality
Pre-drilling works	Noise and Air Quality
Bored pile works for landscape elevated walkway	Noise and Air Quality
Demolition of existing structure and cottage	Noise and Air Quality
Construction of underground works at pedestrian streets	Noise and Air Quality

7.2 The mitigation measures for environmental impact including Air Quality, Construction Noise, Water Quality, Chemical and Waste Management, Landscape and Visual shall be implemented:

- Sufficient watering of the works site with the active dust emitting activities,
- Limitation of the speed for vehicles on unpaved site roads,
- Properly cover the stockpiles,
- Good maintenance to the plant and equipment,
- Use of quieter plant and Quality Powered Mechanical Equipment (QPME),
- Provide movable noise barriers,
- Appropriate desilting/ sedimentation devices provided on site for treatment before discharge,
- Well maintain the drainage system to prevent the spillage of wastewater during heavy rainfall,
- Onsite waste sorting and implementation of trip ticket system,
- Good management and control on construction waste reduction,
- Erection of decorative screen hoarding,
- Strictly following the Environmental Permits and Licenses, and
- Provide sufficient mitigation measures as recommended in Approved EIA Reports.

7.3 The recommended environmental measures proposed in the EM&A Manual (EIA Register No. AEIAR-130/2009) shall be effectively implemented to minimize the potential environmental impacts. The Contractor is reminded to implement the mitigation measures properly.

## **Environmental Site Inspection and Monitoring Schedule for next month**

7.4 The tentative schedule for weekly site inspection and air quality and noise monitoring in the next month is provided in Appendix C.

## **8. CONCLUSIONS**

- 8.1 Environmental monitoring works were performed in the reporting month and all monitoring results were checked and reviewed.
- 8.2 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.3 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.4 Construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 8.5 No complaint was received in the reporting month.
- 8.6 No notification of summons and successful prosecutions was received in the reporting month.
- 8.7 Based on the site inspection and audits, impact air quality and noise monitoring results, it was considered that the mitigation measures were effective to control the potential environmental impacts from the Project during the reporting period.



**Figure**

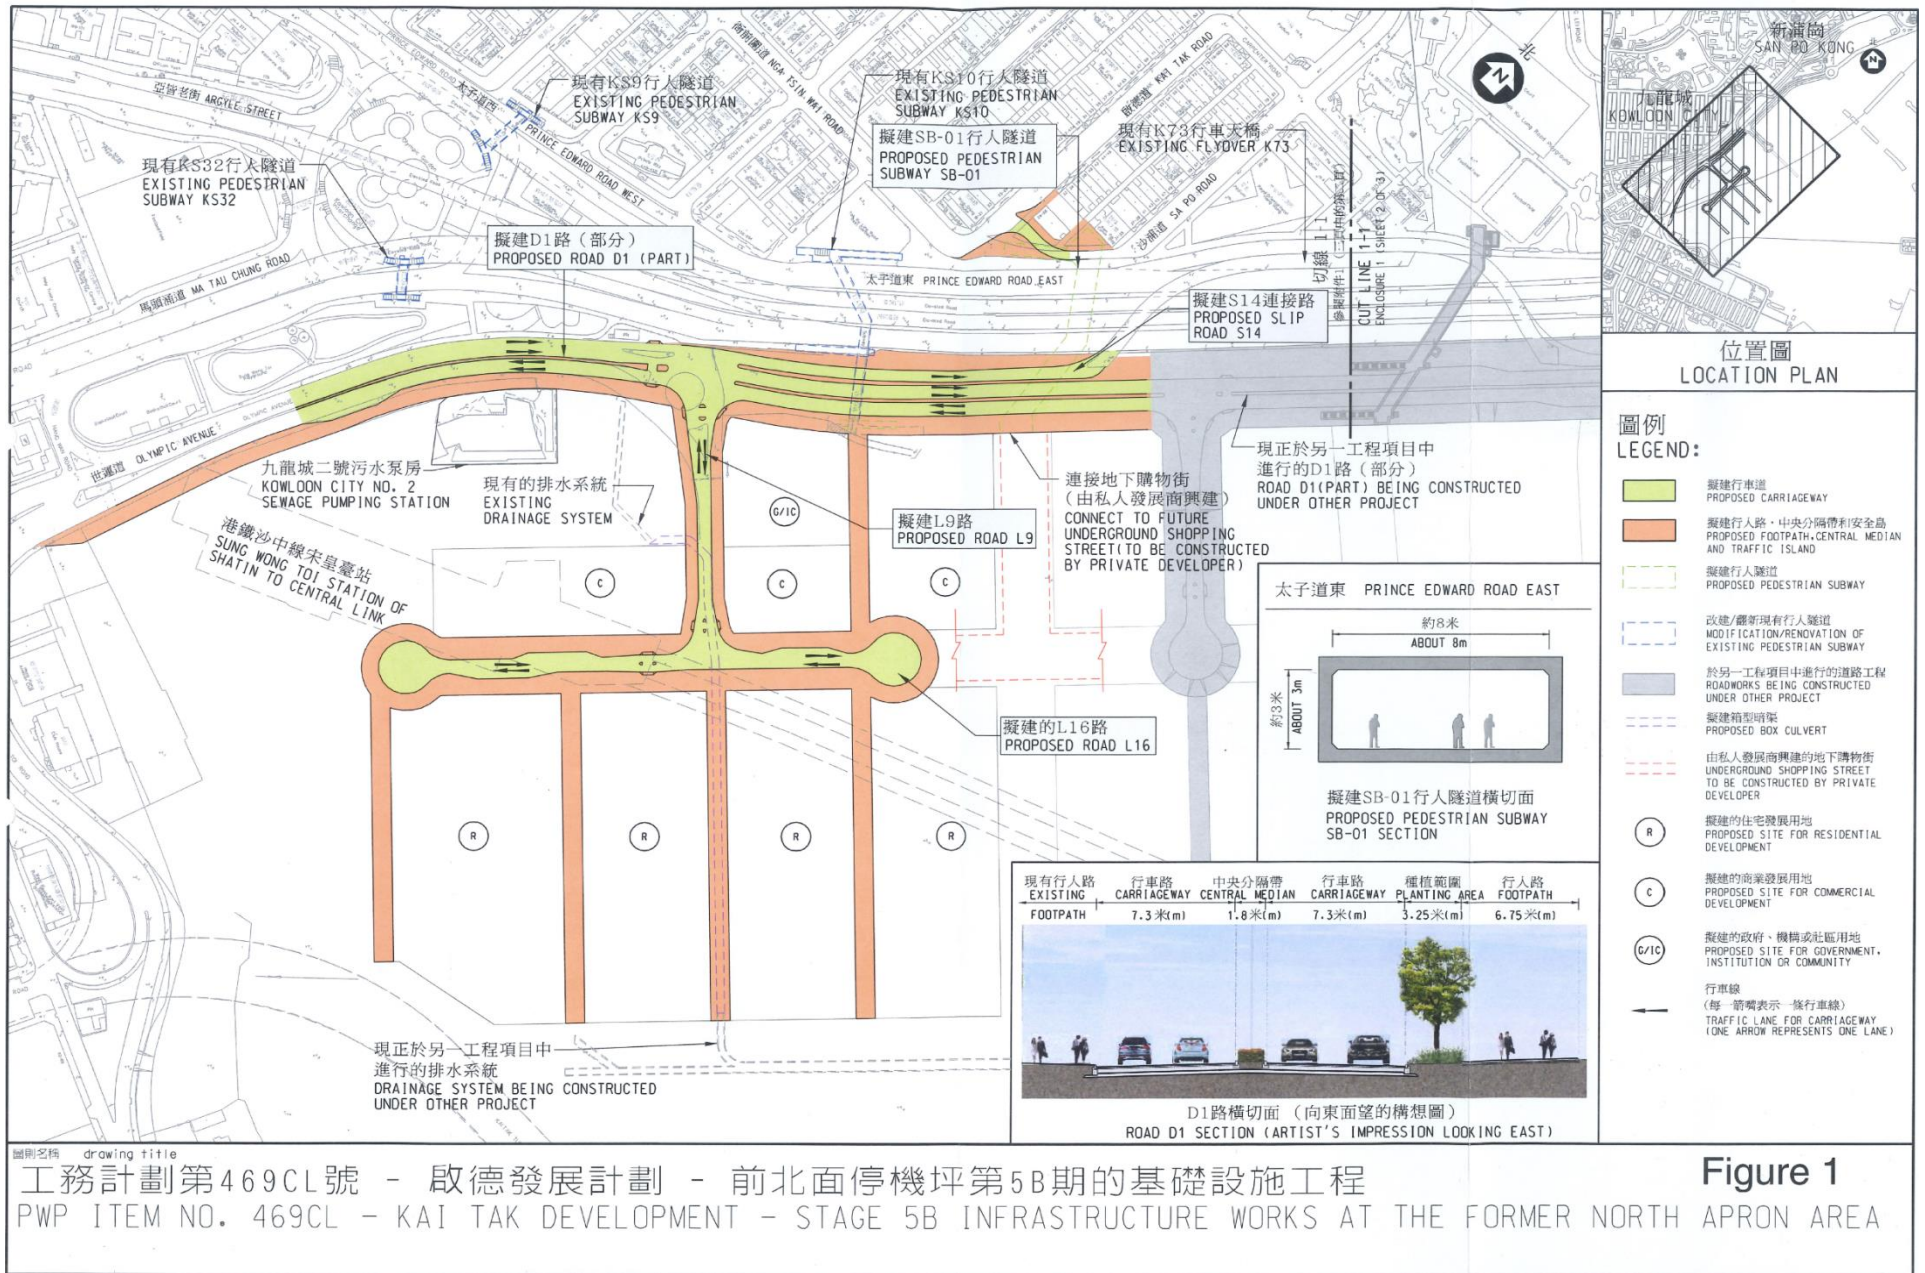


Figure 1 – Proposed works of Contract No. ED/2018/05



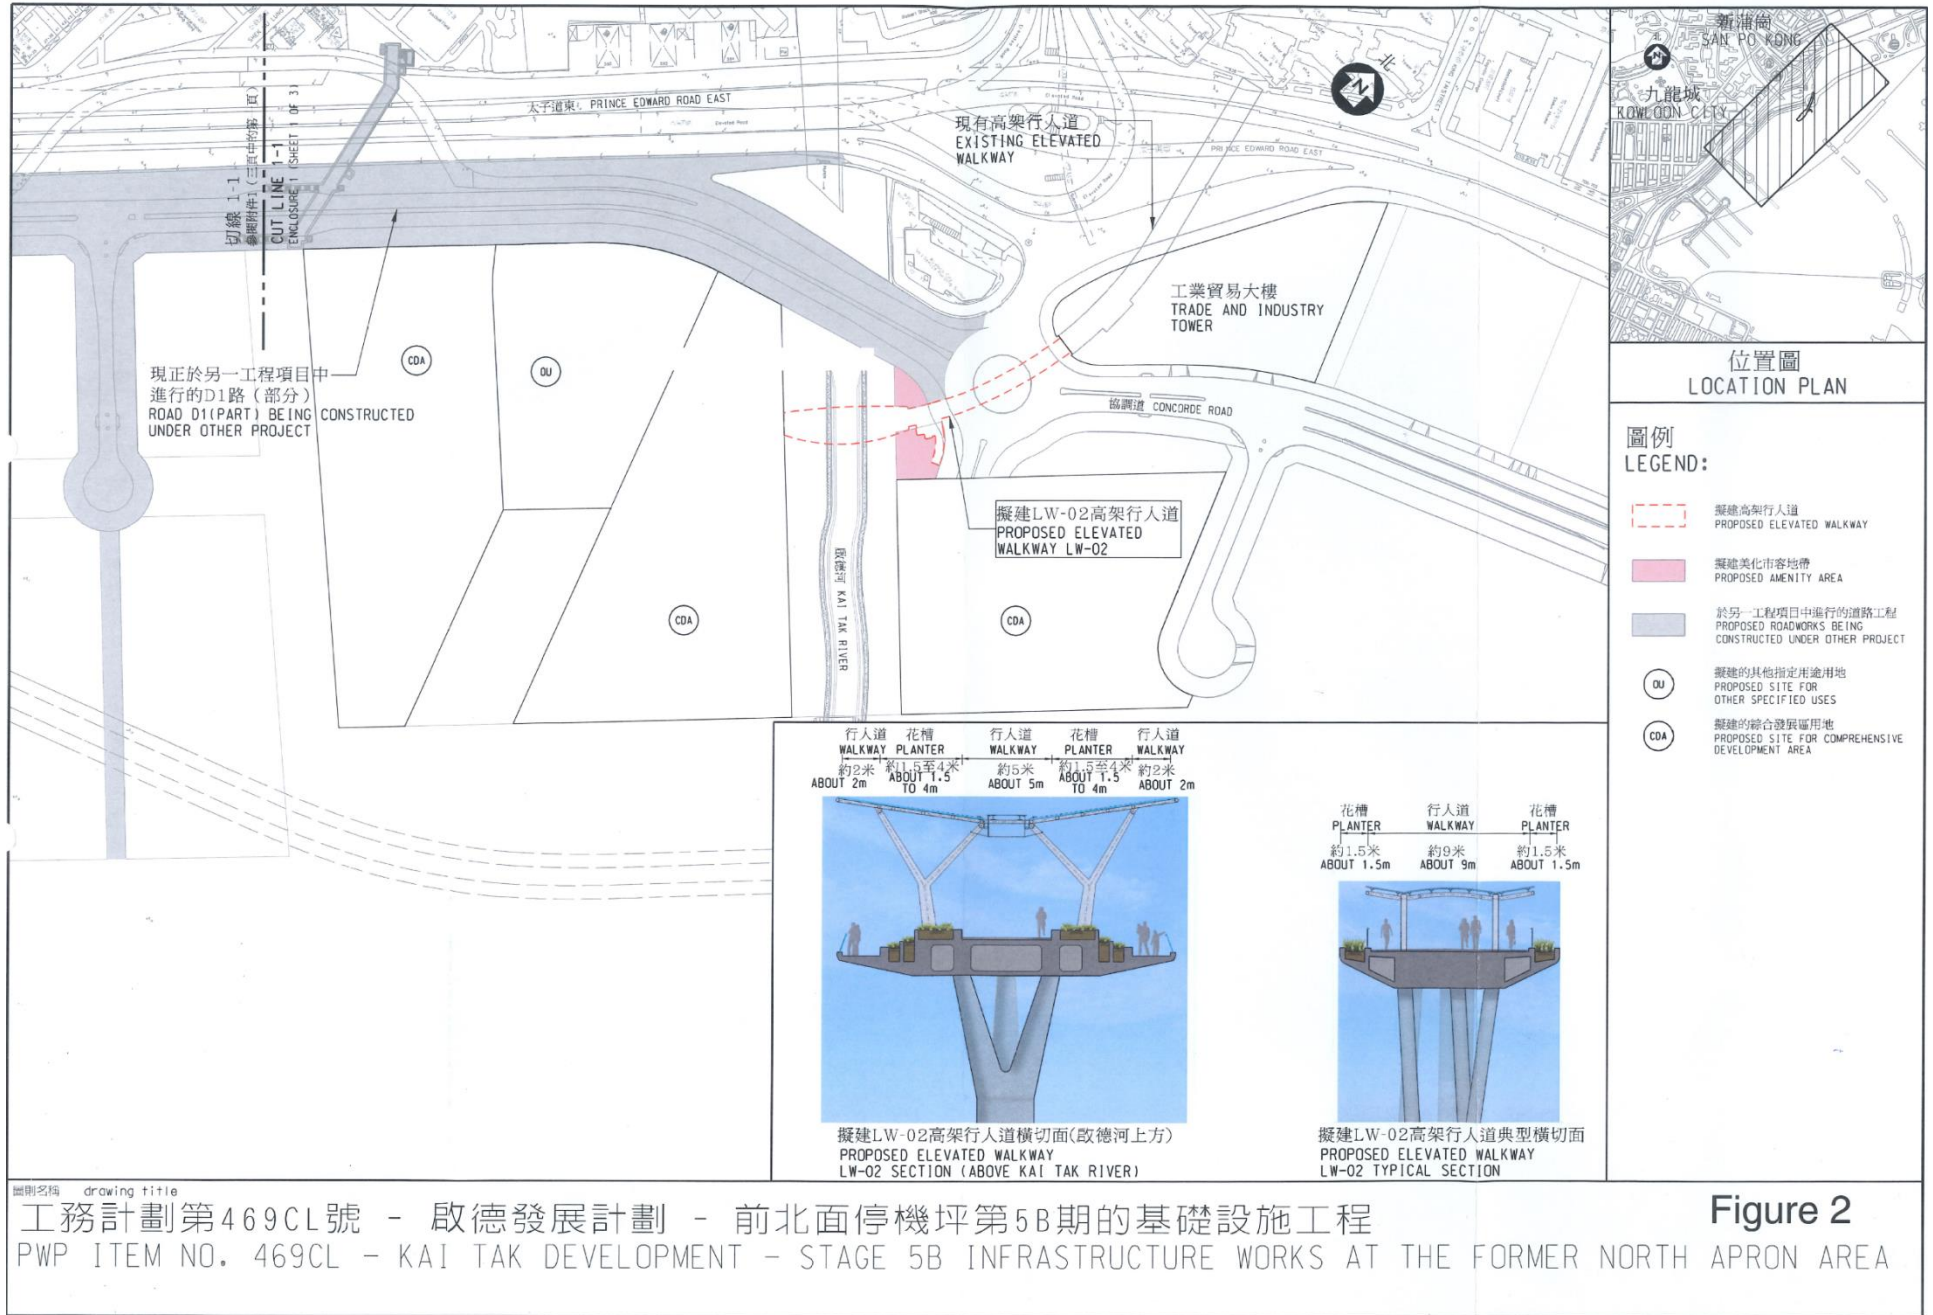


Figure 2

Figure 2 – Proposed works of Contract No. ED/2018/05

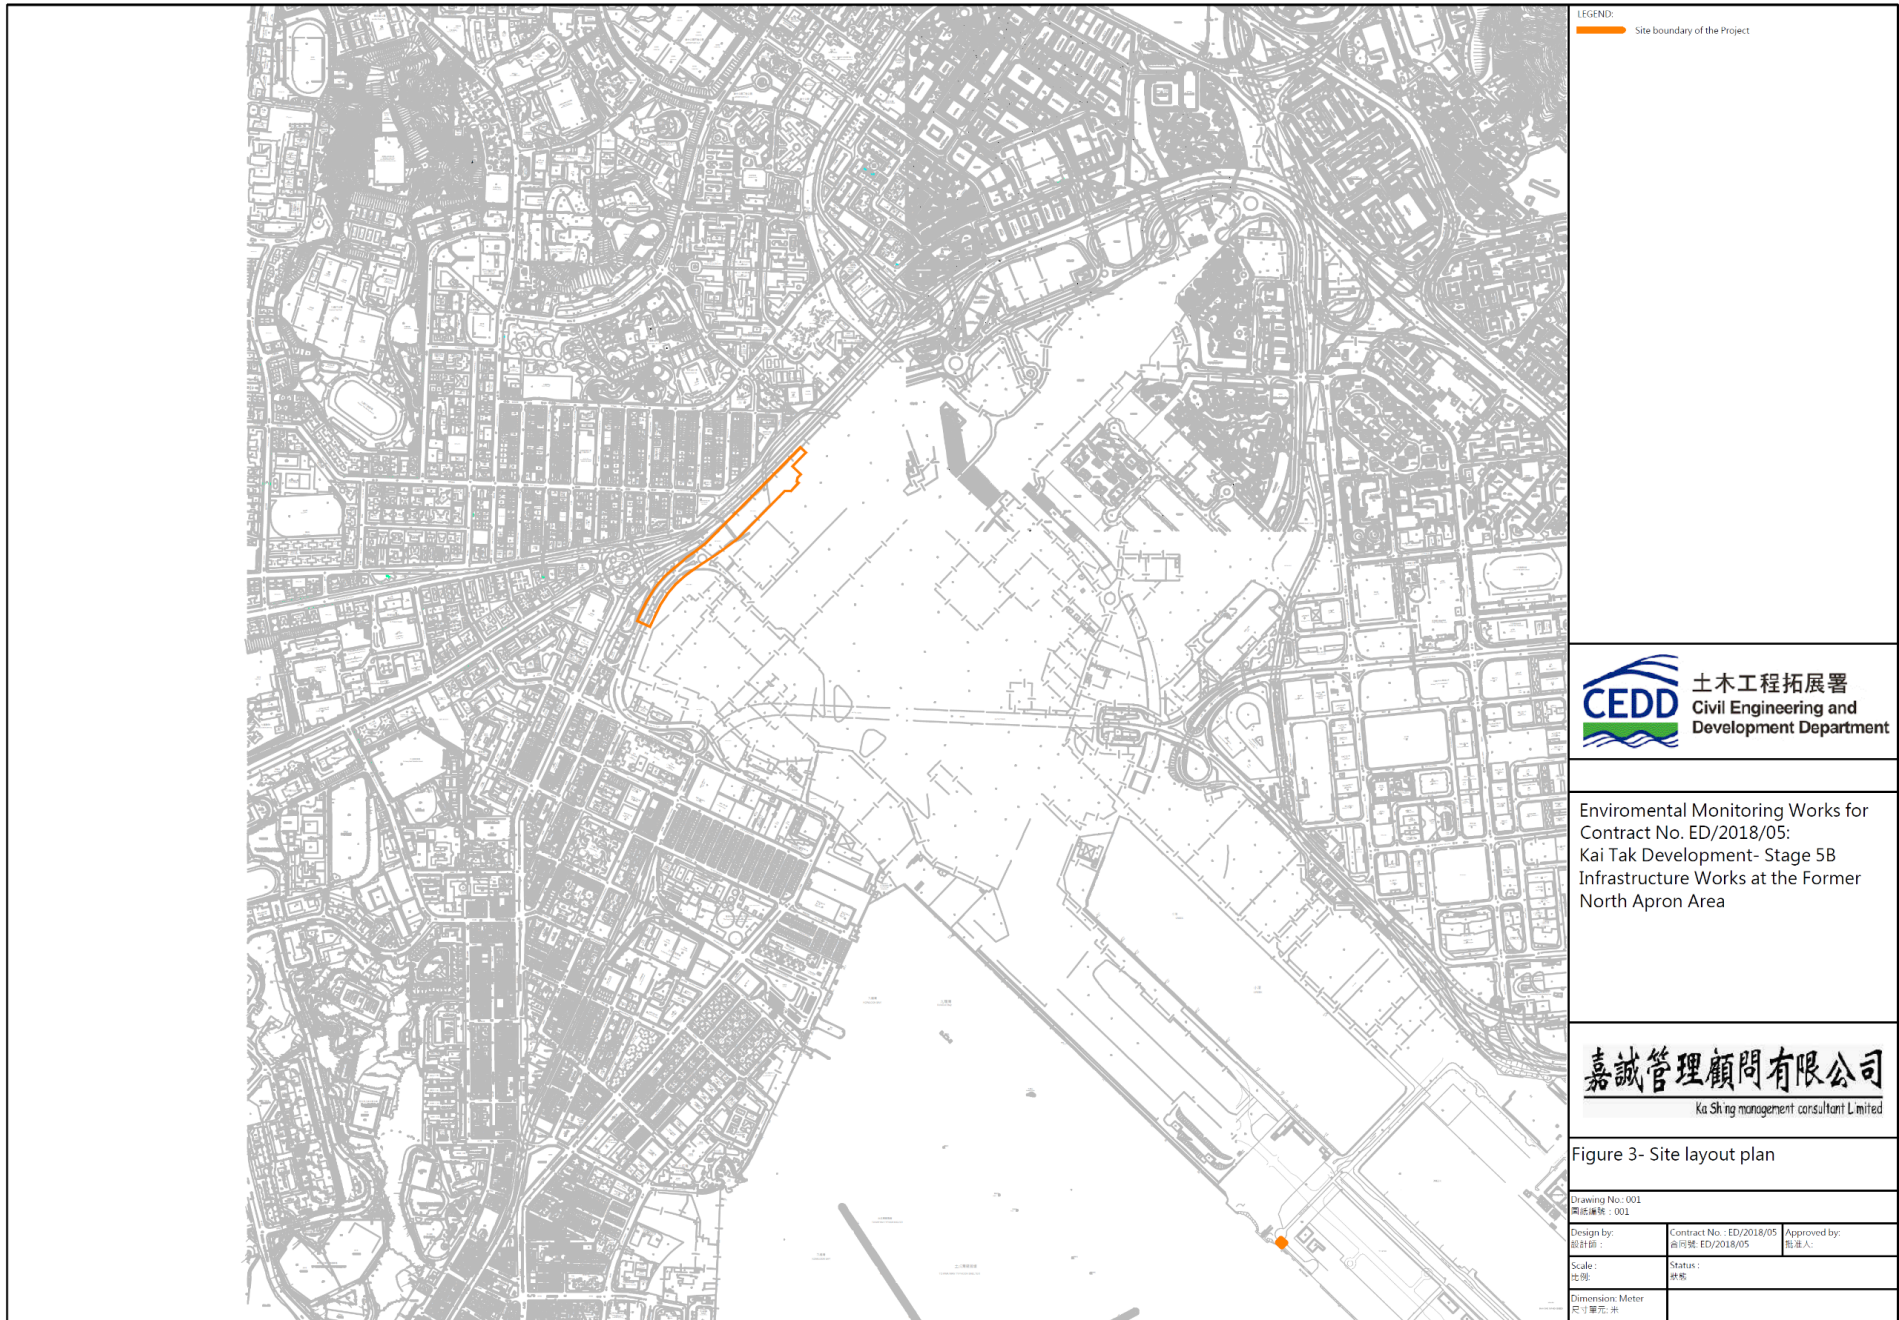


Figure 3 – D1 Road Site Layout Plan



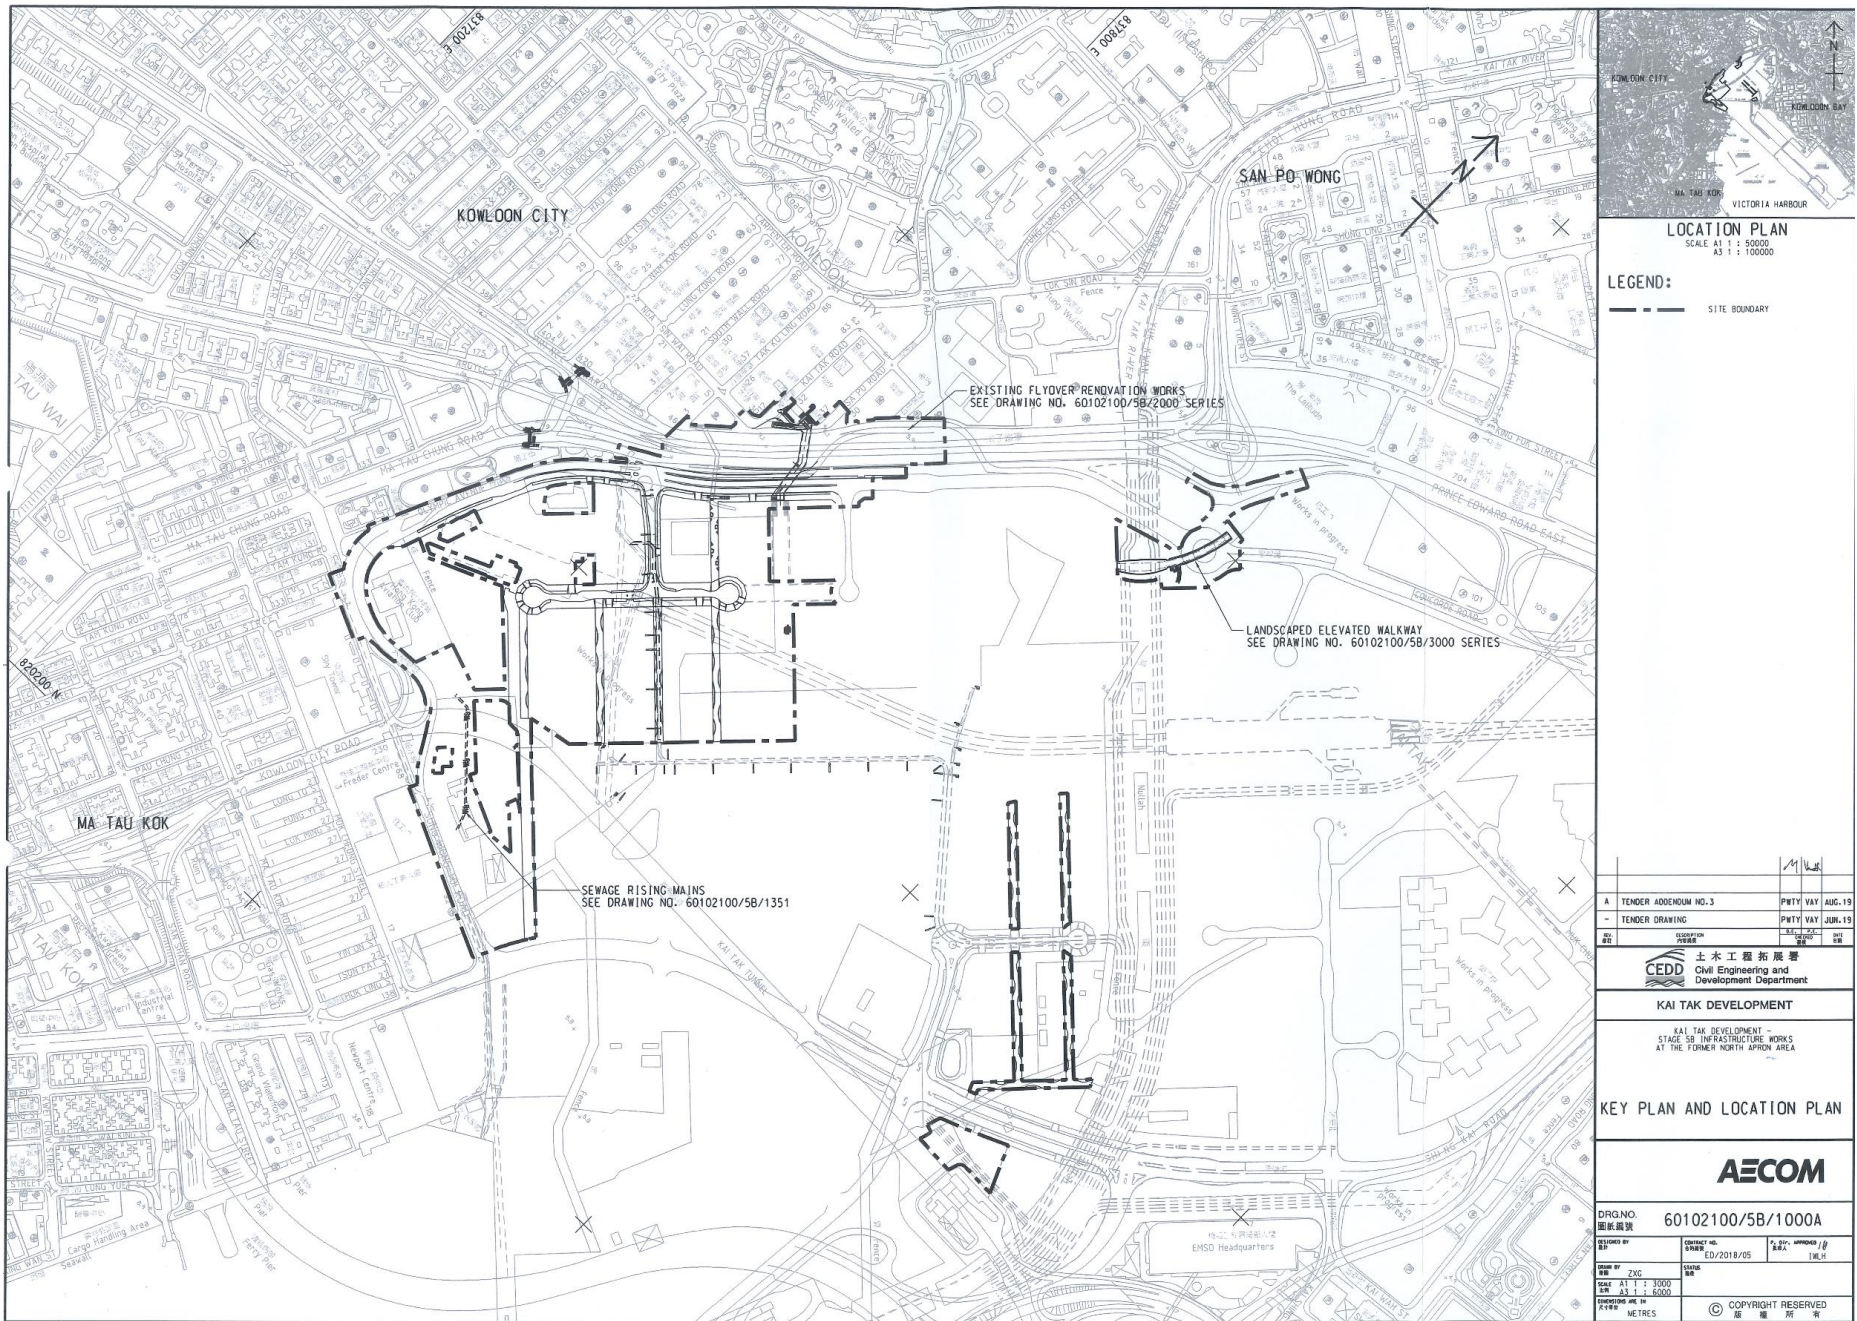


Figure 4 – Site Layout Plan



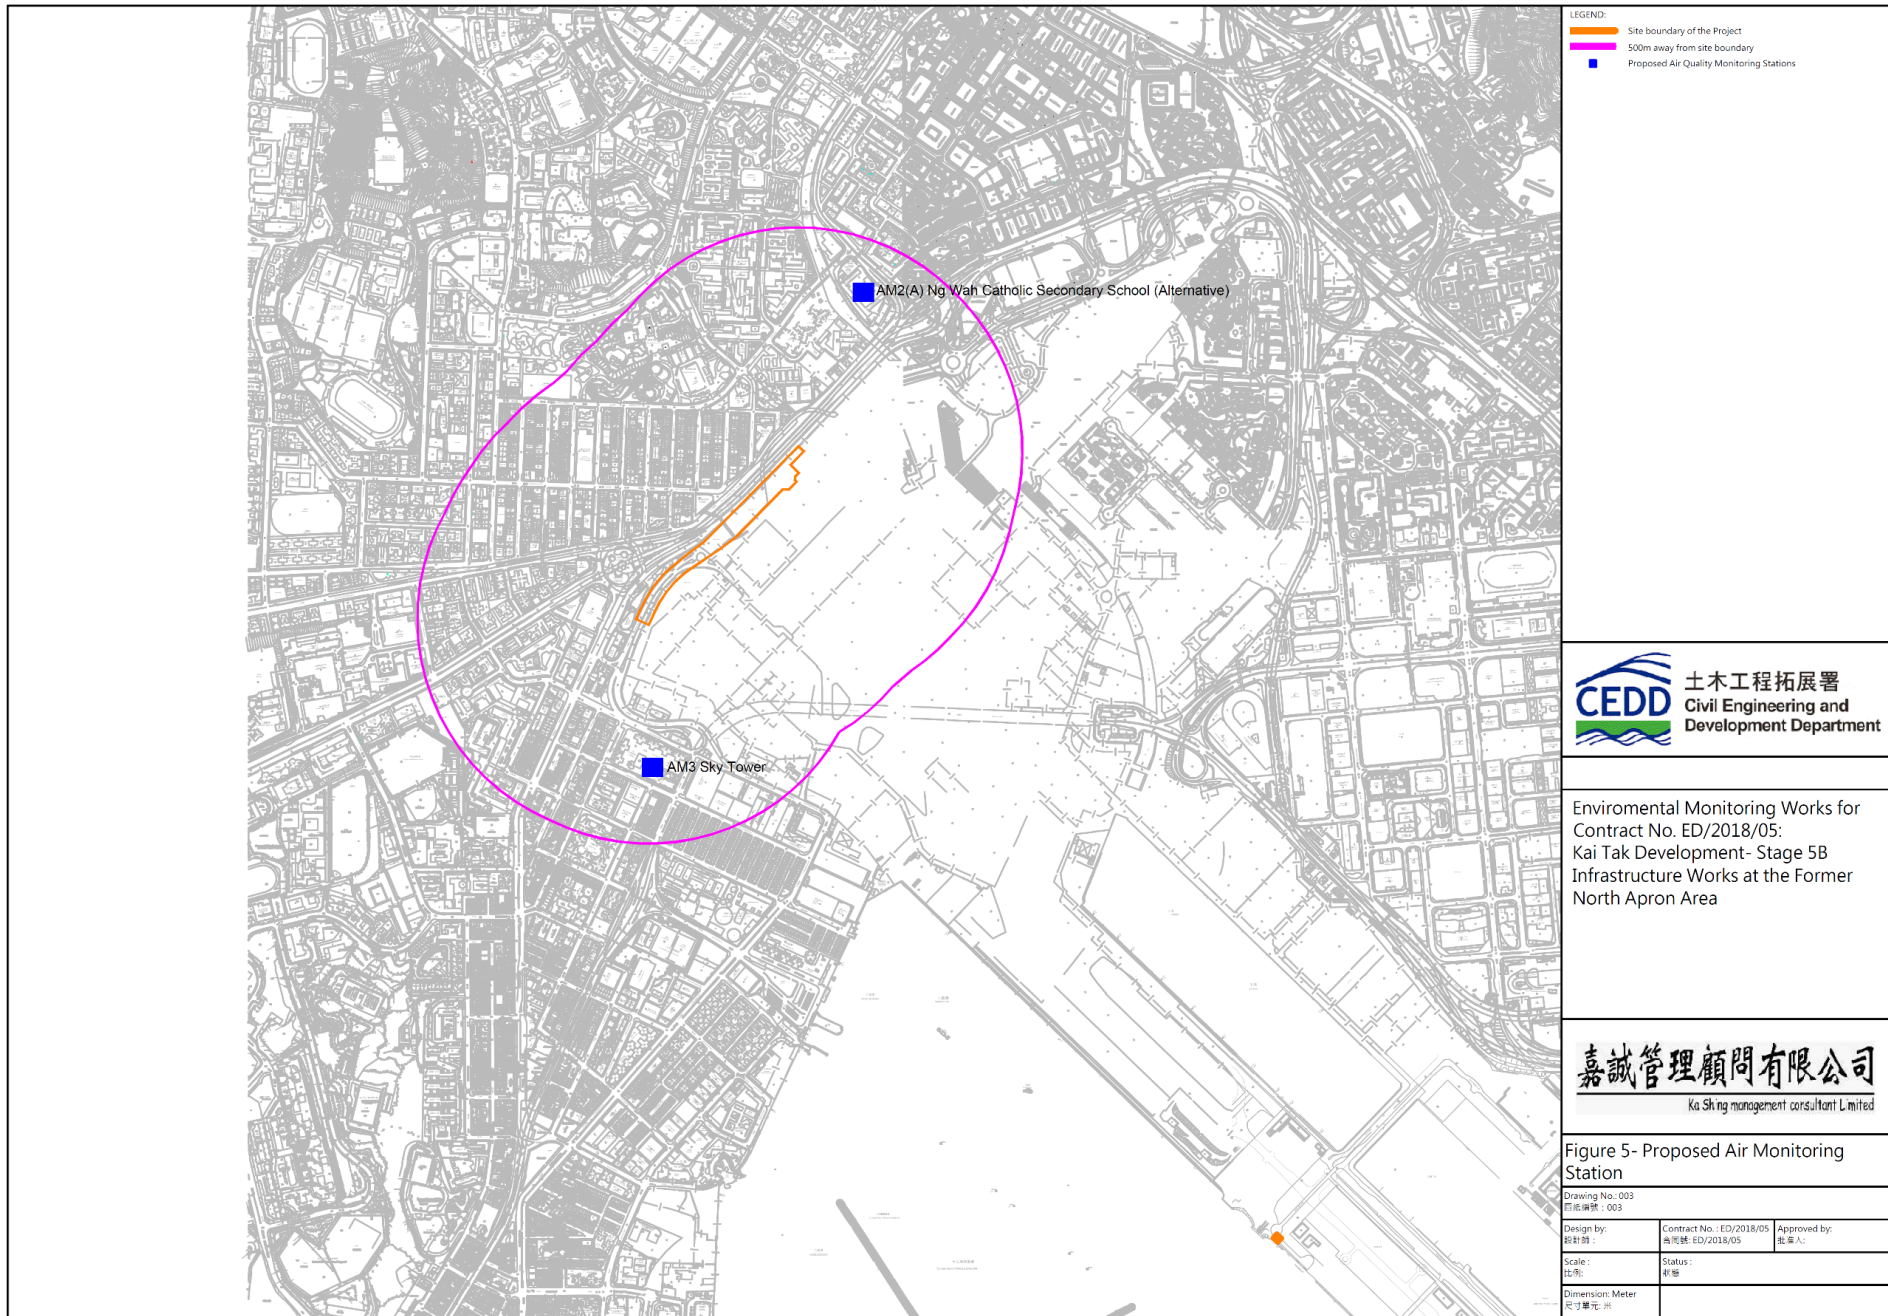


Figure 5 – Air Quality Monitoring Stations

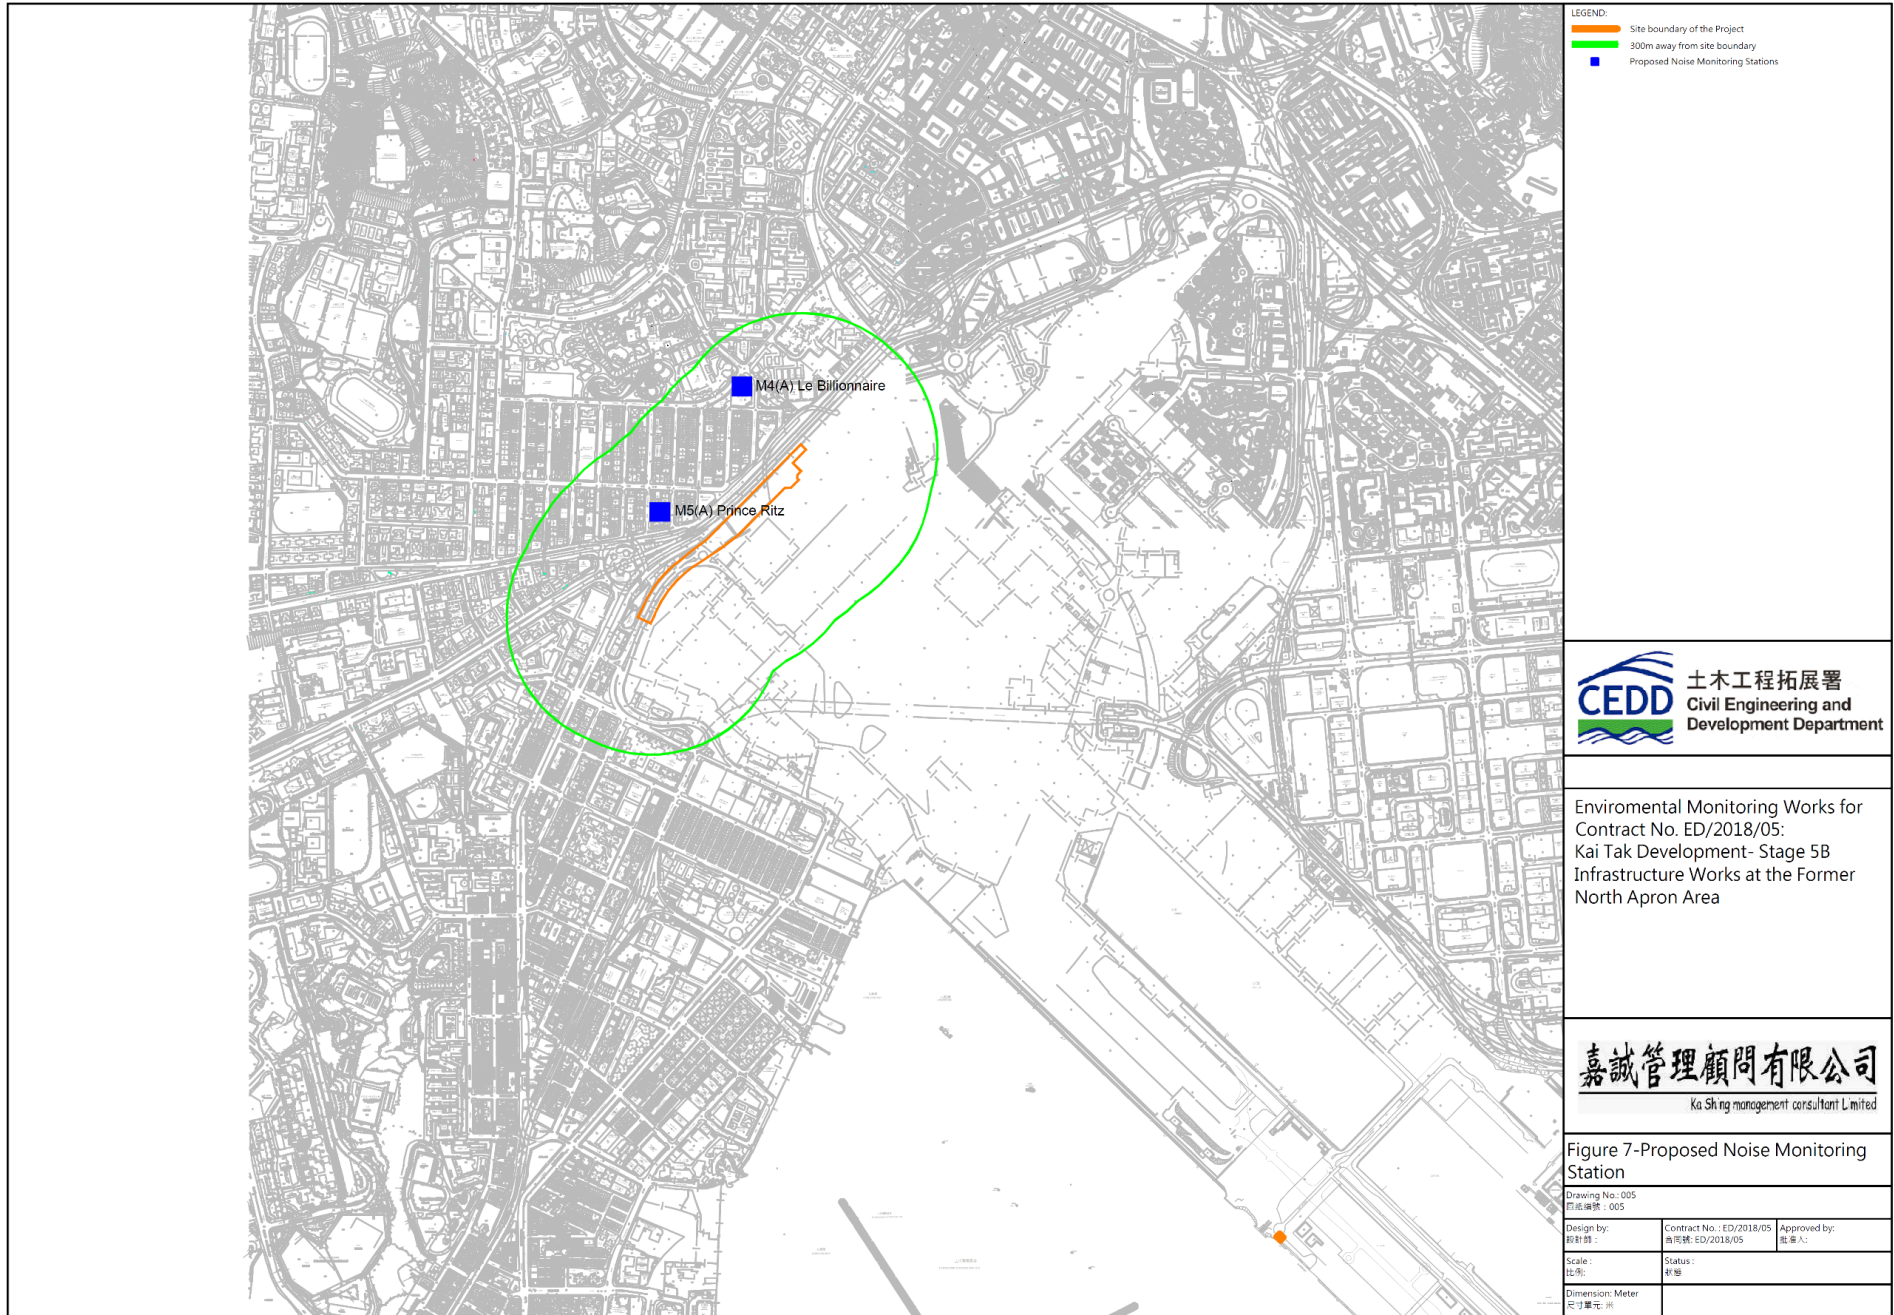


Figure 6 – Noise Monitoring Stations

**Appendix A – Organization Chart of EM&A Team**





# Appendix B – Construction Programme















**Appendix C – Environmental monitoring schedules**



Contract No. EDO 2/2020 Environmental Monitoring at Kai Tak Development – Stage 5B infrastructure works at the former north apron area  
Environmental Monitoring and Weekly Site Inspection Schedule for February 2021

February 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4 Weekly Site Inspection	5	6
7	8	9	10	11 Weekly Site Inspection	12	13
14	15	16	17 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	18 Weekly Site Inspection	19	20
21	22	23 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	24	25 Weekly Site Inspection + SSMC meeting	26	27
28						

NOTE:

1) Measurement schedule may be changed due to unforeseen circumstance (e.g. adverse weather).

**Air Quality Monitoring Station**

AM2(A) Ng Wah Catholic Secondary School  
AM3 - Sky Tower

**Noise Quality Monitoring Station**

M4(A) - Le Billionnaire  
M5(A) - Prince Ritz

Contract No. EDO 2/2020 Environmental Monitoring at Kai Tak Development – Stage 5B infrastructure works at the former north apron area  
Environmental Monitoring and Weekly Site Inspection Schedule for March 2021

March 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	2	3	4 Weekly Site Inspection	5	6 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3
7	8	9	10	11 Weekly Site Inspection	12 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	13
14	15	16	17	18 Weekly Site Inspection 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	19	20
21	22	23	24 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	25 Weekly Site Inspection + SSMC meeting	26	27
28	29 24-hr TSP and 1-hrX3 TSP: AM2(A), AM3 30-min Noise: M4(A), M5(A)	30	31			

NOTE:

1) Site inspection schedule and Impact monitoring schedule may be changed due to unforeseen circumstance (e.g. adverse weather).

**Air Quality Monitoring Station**

AM2(A) Ng Wah Catholic Secondary School  
AM3 - Sky Tower

**Noise Quality Monitoring Station**

M4(A) - Le Billionnaire  
M5(A) - Prince Ritz

**Appendix D – Photographic records**


## Impact Air Quality Monitoring



Measurement setup at AM2(A)




Measurement setup at AM3

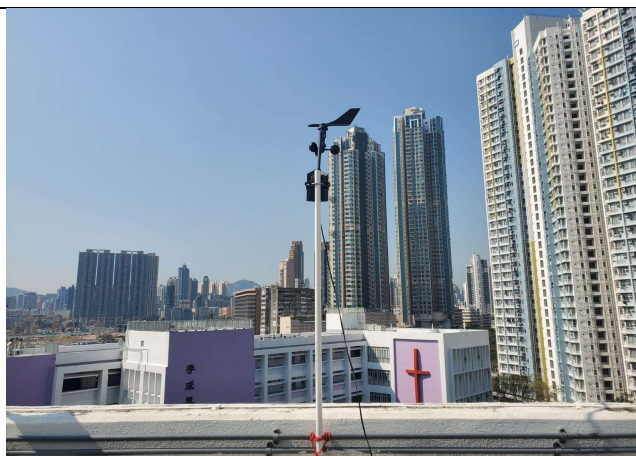

Weather Station at the rooftop of Ng Wah Catholic Secondary School

Impact Noise Monitoring

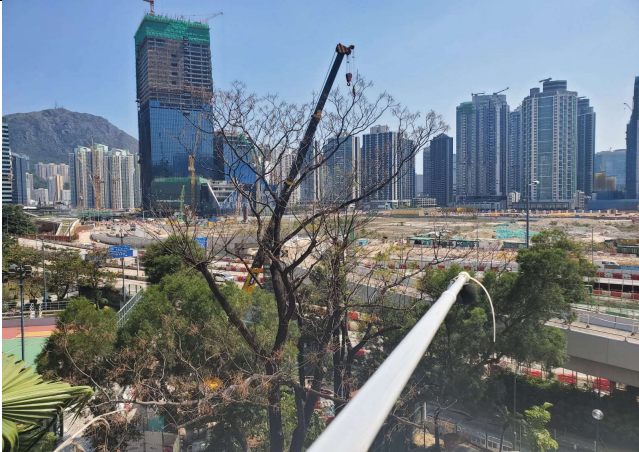

Measurement setup at M4(A)



Measurement setup at M5(A)

**Appendix E – Calibration certificates, catalogue of air quality  
monitoring equipment**



## Catalogue of High Volume Sampler (HVS)



### TSP MFC

Total Suspended Particulate, Mass Flow Controlled



**MFC TSP**  
Ambient Air Sampler

The TE-5170 is a high volume ambient Total Suspended Particulate (TSP) air sampler featuring a mass flow controller (MFC) for accurate and consistent particulate sampling. The mass flow controller adjust the motor speed as the filter media collects particulate to maintain a constant flow rate throughout the entire sample duration. The system utilizes a stainless steel filter holder for use with standard 8" x 10" filter paper. The anodized aluminum shelter and robust electrical components allow the system to operate a continuous 24 hour sample.

**ABOUT US:** Tisch Environmental Inc. Tisch Environmental is the benchmark for high volume air sampling, particulate, metals, volatiles, and specialty monitoring equipment. Since the company's inception in 1953 as General Metal Works, our product line has expanded from the first high volume air sampler to include high-tech and custom samplers. Our clients are professionals from every sector of the regulatory and industrial markets.

- ✔ Meets EPA CFR, Appendix B to Part 50
- ✔ Total Suspended Particulate(TSP)
- ✔ Mass Flow Controlled
- ✔ 7-Day Mechanical Timer
- ✔ Elapsed Time Indicator
- ✔ Aluminum Outdoor Shelter
- ✔ Brush Style Motor
- ✔ Dickson Chart Recorder, 24 Hour
- ✔ Stainless Steel Filter Holder
- ✔ 36-60 CFM
- ✔ Made In USA

Copyright © 2014 Tisch International All Rights Reserved  
www.tischinternational.com



www.tisch-env.com

Tisch Environmental  
145 S. Miami Ave  
Cleveland, OH 45002  
513-487-9000  
sales@tisch-env.com



## TSP MFC

MFC TSP Ambient Air Sampler

### General System Specifications

**Particulate Size:**Total Suspended Particulate (TSP)  
**EPA Designation:** CFR 40 Part 50 Appendix B  
**Flow Controller:** Mass Flow Controller  
**Motor Style:**Brush Style Motor Assembly  
**Pressure Recorder:**Dickson Chart Recorder, 24 hour  
**Timer:**7 Day Mechanical  
**Elapsed Time Indicator:**Mechanical, Hours and Tenths  
**Flow Range:**39-60CFM, 1.09M<sup>3</sup>M-1.68M<sup>3</sup>M  
**Housing:**Anodized Aluminum  
**Filter Holder:**Stainless Steel, 8" x 10"  
**4" Recorder Charts:** Box of 100  
**Filter Holder:** 8" x 10" Stainless Steel with hold down frame

### Applications

US EPA Reference Method Sampling, CFR Appendix J Part 50 Regulatory Compliance  
 Institutional Studies  
 Construction Sites  
 Bridge and Water Tower Painting Sites  
 Fence Line Monitoring  
 Industrial Monitoring  
 Landfill Monitoring  
 Public Health Applications

### Optional Equipment

TE-3000 Filter Holder Cartridge  
 TE-G653 8" x 10" Glass Fiber Filter Media  
 TE-33384 Motor Brush Set (110volt)  
 TE-33378 Motor Brush Set (220volt)  
 TE-116311 Replacement Motor (110volt)  
 TE-116312 Replacement Motor (220volt)  
 TE-106 Recorder Charts  
 TE-160 Recorder Pen Points  
 TE-5018 Gasket 8" x 10"

### Available Models

TE-5170 TSP MFC, 110 Volt 60 Hertz, 8 Amps  
 TE-5170X TSP MFC, 220 Volt 50 Hertz 4 Amps  
 TE-5170XZ TSP MFC, 220 Volts 60 Hertz, 4 Amps

### Calibration Equipment

TE-5028 -Variable Flow Calibration Kit  
 TE-HVC-V Xcalibrator HiVol Calibrator

### Physical Specifications

**Weight:** 75lbs, Shelter  
**Shipping Dimensions:** 46"W x 23"L x 20" H, Shelter  
 19"W x 19"L x 20"H, Lid  
**Assembled Dimensions:** 28"W x 28"L x 61"H

Copyright © 2014 Tisch International All Rights Reserved  
www.tischinternational.com

www.tisch-env.com



## Calibration Certificate of HVS

### Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2021020602 Date of calibration : 06/02/2021

Location : Sky Tower Sampler : TE-5170X

Calibration Data Serial Numbers : 4687

Ambient barometric pressure, Pa = 762.8 (mmHg) Ambient temperature, Ta = 296.55 (deg K)


Qstd Slope, m = 2.04882 Qstd Intercept, b = -0.011270

Calibration Curve

Plate No.	H <sub>2</sub> O (in)	Qstd (m <sup>3</sup> / min)	I (chart)	IC (corrected)
18	7.60	1.357	49.0	49.21
13	6.50	1.255	45.0	45.19
10	5.40	1.145	40.0	40.17
7	3.70	0.948	34.0	34.15
5	2.50	0.781	29.0	29.13

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1/m1 [(I) (\text{Sqrt} ((Pav / 760) (298 / Tav))) - b1]$	34.711	1.4846	0.9964

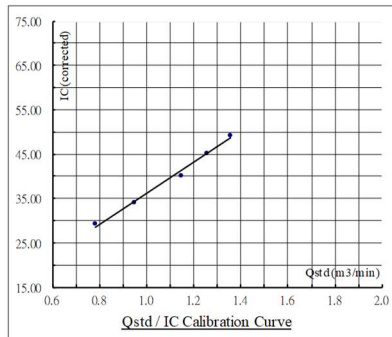

Calibration curve requirements : (A).  $r > 0.990$ ; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m<sup>3</sup> / min).

Remark :  $Qstd (m^3 / min) = 1/m [ \text{Sqrt} (H_2O (Pa / 760) (298 / Ta)) - b ]$

$IC (corrected) = I [ \text{Sqrt} ((Pa / 760) (298 / Ta)) ]$

$FLOW (corrected) = \text{Sqrt} (FLOW (mano) (Pa / 760) (298 / Ta))$

Calibrated by : Ben Poon 06/02/2021 Name : Tommy Wong 06/02/2021

Name : ( Ben Poon ) Name : ( Tommy Wong )

Form No. NS-HVS-CALdd 16 012020

### Air Sampler Calibration Curve Plotting & Calculation (Dickson recorder)

Calibration curve ref. No. : ATSPC-01-2021020604 Date of calibration : 06/02/2021

Location : Ng Wah Catholic Secondary School Sampler : TE-5170X

Calibration Data Serial Numbers : 4360

Ambient barometric pressure, Pa = 762.8 (mmHg) Ambient temperature, Ta = 296.55 (deg K)


Qstd Slope, m = 2.04882 Qstd Intercept, b = -0.011270

Calibration Curve

Plate No.	H <sub>2</sub> O (in)	Qstd (m <sup>3</sup> / min)	I (chart)	IC (corrected)
18	7.50	1.348	47.0	47.20
13	6.60	1.265	44.0	44.19
10	5.40	1.145	41.0	41.18
7	3.80	0.961	37.0	37.16
5	2.30	0.749	32.0	32.14

Subsequent calculation of sampler flow

Method	Calibration equation	Slope, m	Intercept, b	Corr. coeff., r
Dickson recorder	$Qstd = 1/m1 [(I) (\text{Sqrt} ((Pav / 760) (298 / Tav))) - b1]$	24.437	13.6493	0.9973

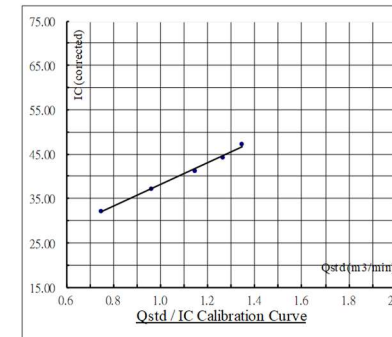

Calibration curve requirements : (A).  $r > 0.990$ ; (B). At least 3 Qstd numbers are in the TSP range (1.1 - 1.7 m<sup>3</sup> / min).

Remark :  $Qstd (m^3 / min) = 1/m [ \text{Sqrt} (H_2O (Pa / 760) (298 / Ta)) - b ]$

$IC (corrected) = I [ \text{Sqrt} ((Pa / 760) (298 / Ta)) ]$

$FLOW (corrected) = \text{Sqrt} (FLOW (mano) (Pa / 760) (298 / Ta))$

Calibrated by : Ben Poon 06/02/2021 Checked by : Tommy Wong 06/02/2021

Name : ( Ben Poon ) Name : ( Tommy Wong )

Form No. NS-HVS-CALdd 16 012020



# Calibration Certificate of HVS



<b>RECALIBRATION DUE DATE:</b>
<b>July 17, 2021</b>

## Certificate of Calibration

Calibration Certification Information			
Cal. Date: July 17, 2020	Rootsmeter S/N: 438320	Ta: 296 °K	
Operator: Jim Tisch		Pa: 753.4 mm Hg	
Calibration Model #: TE-5025A	Calibrator S/N: 0006		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4300	3.2	2.00
2	3	4	1	1.0100	6.4	4.00
3	5	6	1	0.9010	7.9	5.00
4	7	8	1	0.8570	8.8	5.50
5	9	10	1	0.7090	12.8	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
0.9937	0.6949	1.4128	0.9958	0.6963	0.8865
0.9895	0.9797	1.9980	0.9915	0.9817	1.2536
0.9875	1.0960	2.2338	0.9895	1.0982	1.4016
0.9863	1.1509	2.3428	0.9883	1.1532	1.4700
0.9810	1.3837	2.8255	0.9830	1.3865	1.7729
<b>QSTD</b>	m=	<b>2.04882</b>	<b>QA</b>	m=	<b>1.28293</b>
	b=	<b>-0.01127</b>		b=	<b>-0.00707</b>
	r=	<b>0.99999</b>		r=	<b>0.99999</b>

Calculations	
Vstd= ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va= ΔVol((Pa-ΔP)/Pa)
Qstd= Vstd/ΔTime	Qa= Va/ΔTime
For subsequent flow rate calculations:	
Qstd= 1/m $\left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} - b \right)$	Qa= 1/m $\left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} - b \right)$

Standard Conditions
Tstd: 298.15 °K
Pstd: 760 mm Hg
Key
ΔH: calibrator manometer reading (in H2O)
ΔP: rootsmeter manometer reading (mm Hg)
Ta: actual absolute temperature (°K)
Pa: actual barometric pressure (mm Hg)
b: intercept
m: slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.  
145 South Miami Avenue  
Village of Cleves, OH 45002

[www.tisch-env.com](http://www.tisch-env.com)  
TOLL FREE: (877)263-7610  
FAX: (513)467-9009

## Catalogue of Dust Meter (TSI Sidepak AM510)

The SidePak AM510 monitor's easy-to-read display shows your data as both real-time aerosol mass-concentration and 8-hour time-weighted average (TWA). With its convenient data logging and long battery life, the AMS10 is also ideal for extended sampling. The easy-to-use TrakPro Data Analysis Software lets you create effective graphs and reports.

### User Friendly

- + Small, lightweight and quiet to maximize worker acceptance
- + Rugged design with secure belt clip
- + Easy-to-understand user interface with only four keys
- + Lockable keypad prevents tampering while sampling
- + User-adjustable sample flow rate
- + Define, label and store multiple calibration constants
- + Easy-to-read LCD display
- + Convenient, threaded tripod socket accommodates area sampling

### Advanced Features

- + Smart Battery Management System provides precise run time information, maximizes battery capacity and speeds charging
- + Integrated pump allows use of size-selective aerosol inlet conditioners
- + Built-in impactors let you choose "none," 1.0, 2.5 or 10-micron cut off
- + 10-mm Dorr-Oliver cyclone for respirable sampling
- + Display shows real-time concentrations (mg/m<sup>3</sup>) and "on-the-fly" TWA as you data log
- + Display statistics: max, min and average readings, elapsed time and 8-hour TWA

### Quick and Easy Reports

- + Convenient preprogramming for occupational exposure sampling
- + Data log for long periods and store multiple tests
- + Analyze data, print graphs and create reports with TrakPro Data Analysis Software
- + USB port lets you conveniently connect to your computer

### Power to Spare

- + Long-lasting NiMH rechargeable battery packs eliminate "memory" issues
- + Choice of rechargeable NiMH smart battery packs or AA-cell pack

### Model AMS10

#### SidePak Personal Aerosol Monitor

#### Sensitivity

Sensor Type 90° light scattering, 670 nm laser diode  
 Aerosol Concentration Range 0.001 to 20 mg/m<sup>3</sup> (calibrated to respirable fraction of ISO 12103-1, A1 test dust)  
 Particle Size Range 0.1 to 10 micrometer (µm)  
 Minimum Resolution 0.001 mg/m<sup>3</sup>  
 Zero stability ±0.001 mg/m<sup>3</sup> over 24 hours using 10-second time-constant  
 Temperature Coefficient Approximately +0.0005 mg/m<sup>3</sup> per °C (for variations from temperature at which instrument was last zeroed)

#### Flow Rate

Range User-adjustable, 0.7 to 1.8 liters/min (L/min)

#### Temperature Range

Operating Range 32 to 120°F (0 to 50°C)  
 Storage Range -4 to 140°F (-20 to 60°C)

#### Operational Humidity

0 to 95% RH, non-condensing

#### Time Constant (LCD display)

Range User-adjustable, 1 to 60 seconds

#### Data Logging

Data Points Approx. 31,000  
 Logging Interval User-adjustable, 1 second to 1 hour

#### User-Select Calibration Factors

Factory Setting 1.0 (non-adjustable)  
 User-defined Settings 3, with user-defined labels  
 Range 0.1 to 10.0, user-adjustable

#### Physical

External Dimensions 4.2 x 3.7 x 2.8 in. (106 x 92 x 70 mm) with 801723, 801724, 801729 or 801743 battery  
 5.1 x 3.7 x 2.8 in. (130 x 92 x 70 mm) with 801708, 801722, 801728, 801735, or 801736 battery  
 Weight 16 oz (0.46 kg) with 801723, 801724, 801729 or 801743 battery  
 19 oz (0.54 kg) with 801708, 01722, 801728, 801735, or 801736 battery  
 Display 2 line x 12 character LCD  
 Tripod Socket 1/4"-20 female thread

#### Power Supply/Charger (P/N 2613210)

Input Voltage Range 100 to 240 VAC, 50 to 60 Hz  
 Output Voltage 9 VDC @ 1.0 A

### Maintenance

Factory Clean/Calibrate Recommended annually  
 User Zero Calibration Before each use  
 User Flow Calibration As needed

### Communications Interface

Type USB 1.1  
 Connector, Instrument USB Mini-B (socket)

### Minimum Computer Requirements for TrakPro™ Data Analysis Software

Communications Port Universal Serial Bus (USB) v 1.1 or higher  
 Operating System Microsoft Windows® XP, or 7 (32-bit or 64-bit) operating systems

### Battery Performance

Battery Options	Charge Time (hrs)*	Intrinsic Safety Rating	Run Time (hrs @ 1.7 L/min)
1600 mAh NiMH Pack, 4.8 V (P/N 801723)	3.0	No	7.1
1650 mAh NiMH Pack, 4.8V (P/N 801724, 801729 or 801743)	3.5	CSA**	7.5
2700 mAh NiMH Pack, 4.8 V (P/N 801722 or 801728)	5.5	No	12.0
2700 mAh NiMH Pack, 4.8 V (P/N 801735)	5.5	No	12.0
6-Cell AA-size Alkaline Pack*** (P/N 801708 or 801736 with six user-supplied AA cells)	N/A	No	22.5


\*Of a fully depleted battery

\*\*All dust plugs and dust gaskets must be installed.

\*\*\*Using Energizer AA-size E91 alkaline batteries.

### Battery Level Indicator

The Smart Battery Management System™ technology utilizes a built-in "gauge" in the SidePak™ battery packs. The gauge monitors battery capacity and calculates run time information by dividing capacity of the battery (mAh) by the instantaneous current consumed by the instrument (mA). This calculation is correct for current operating conditions and can change due to current (mA) consumption or changes in battery capacity.

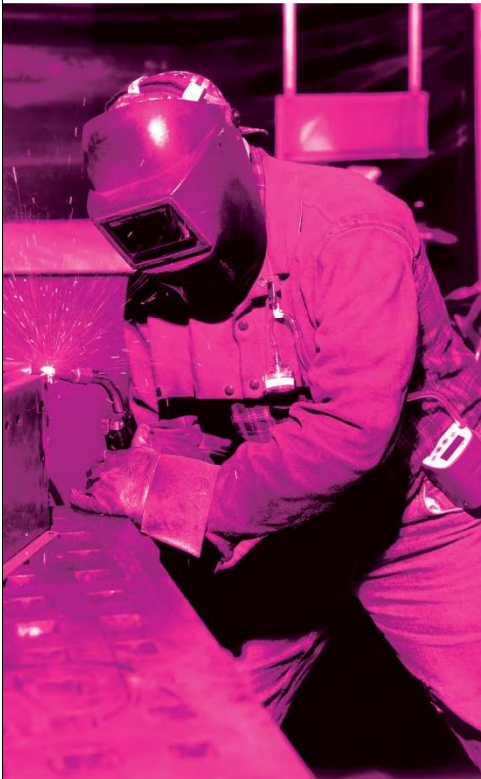



## Calibration Certificate of Dust Meter (TSI Sidepak AM510)

**CERTIFICATE OF CALIBRATION AND TESTING**  
TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA  
 Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

<b>Environment Conditions</b>		<b>Model</b>	<b>AM510</b>
Temperature	74.49 (23.6) °F (°C)	<b>Serial Number</b>	<b>11108001</b>
Relative Humidity	27.1 %RH		
Barometric Pressure	29.25 (990.5) inHg (hPa)		

As Left       In Tolerance  
 As Found       Out of Tolerance

**Concentration Linearity Plot**  

○ = In Tolerance  
● = Out of Tolerance

System ID: DT1101-02

CONCENTRATION				Unit: mg/m <sup>3</sup>			
#	STANDARD	MEASURED	ALLOWABLE RANGE	#	STANDARD	MEASURED	ALLOWABLE RANGE
1	1.868	1.795	1.681-2.055	3	0.076	0.071	0.053-0.099
2	0.266	0.266	0.226-0.306	4	14.397	14.344	12.957-15.837

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass per standard ISO 12103-1, 31 test dust (Arizona dust). Our calibration ratio is greater than 1:1.

<b>Measurement Variable</b>	<b>System ID</b>	<b>Last Cal.</b>	<b>Cal. Due</b>	<b>Measurement Variable</b>	<b>System ID</b>	<b>Last Cal.</b>	<b>Cal. Due</b>
DC Voltage	E003314	01-15-20	01-31-21	Photometer	E005612	08-19-20	02-28-21
Microbalance	M001324	10-16-20	10-31-22	Pressure	E003511	10-26-20	10-31-21
Flowmeter	E005140	01-09-20	01-31-21	DC Voltage	E003315	01-15-20	01-31-21

Calibrated Date

October 30, 2020

### Personal Aerosol Monitor Performance check with High Volume Sampler

Performance Check ref No. : AS0210201-2      Report Issue Date: 01/02/2021  
 Date of performance check : 25/01/2021

**Objective:**


A dust meter and a Total Suspended Particulate High Volume Air Sampler (HVS) were placed together to measure the Total Suspended Particulate (TSP) concentrations simultaneously to check the performance.

**Equipment Used:**

Equipment	Manufacturer and Model	Serial Number
Personal Aerosol Monitor	TSI AM510 Sidepak	11108001
Total Suspended Particulate High Volume Air Sampler	GS2310	10346

**Result:**

Equipment	Measurement Result, µg/m <sup>3</sup>			
TSI AM510 Sidepak	70	157	242	341
High Volume Air Sampler (HVS)	53	131	202	281

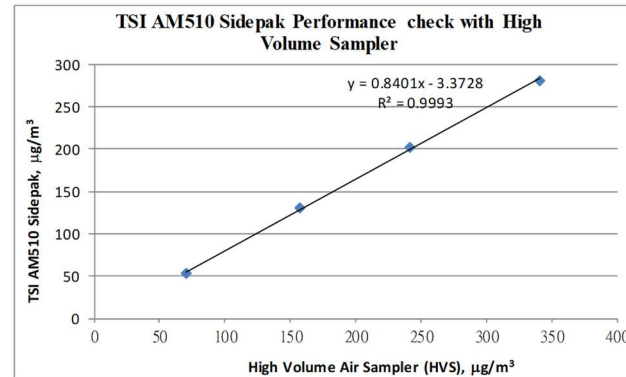

Tested by :      01/02/2021      Checked by :      01/02/2021  
 Name : ( Ben Poon )      Name : ( Tommy Wong )





## Catalogue of Wind Logger

### General information

The anemometer converts the wind speed into electrical signals. These signals are induced by a Reed-contact, which closes through the effect of one magnet.

The magnet, situated on the cup-star, passes the Reed-contact thus forming a frequency dependent on the number of cup-star revolutions, which corresponds to the wind speed.

The wind vane uses a 20kOhm potentiometer

#### **Material**

Wind Vane and Control Head..... UV-resistant ABS  
Wind Cups ..... Polycarbonate  
Anemometer Arm..... Black-anodized aluminium  
Dimensions ..... 470 mm x 191 mm x 121 mm  
Weight ..... 1.332 kg

#### Technical Data - Anemometer

Measuring Range : 1...67m/s  
Accuracy : Expected 2%, guarantee  $\pm 5\%$   
Electronic Output : 0...100Hz at 100.6m/s  
Resolution : 0.1m/s – wind run  
Type of Contact : 1 Reed-contact  
Load : max. 40m/s  
Contact Load : max. 12V DC, max 0.1A

#### Technical Data - Wind vane

Wind Direction : 0° to 360°, 360° = 20kOhm  
Accuracy : Wind Direction  $\pm 7^\circ$   
Wind Direction : 1° (0° to 355°), 22.5° between compasses

Logic Energy Ltd.

[www.logic-energy.com](http://www.logic-energy.com)

### Specification Report

Name : Pro-D Anemometer  
Type No : Reed Switch  
Instrument Number : 1446101  
Order No :  
Measuring Range : 4, 6, 8, 10, 12, 14 m/s

We hereby confirm that the above mentioned instrument was manufactured and tested according to:

**DIN EN ISO 9001**, under the observation of a certified quality assurance system.

The measuring installations used for calibration are regularly calibrated and are based on the national or international standards.

Should no national standards exist, the measuring procedure corresponds with the technical regulations and norms valid at the time of measurement.

#### Confirmation

The standard reaction of the cup-stars is caused by the standardised type of the anemometer as well as narrow tolerance of production.

#### Accuracy

1...10m/s: +/- 0.5m/s  
4...14m/s: resp. +/- 5% of mv.

Further more each anemometer has been checked in a specific test for the whole range about: Output frequency of the reed contact.

Logic Energy Ltd.

[www.logic-energy.com](http://www.logic-energy.com)

## Calibration Certificate of Wing Logger



### Calibration Certificate

**Certificate No.: CC0092010**

**1. Description**

Calibration item :	a) Wind speed b) Wind direction
Equipment description :	Wind Logger with Pro-D sensor
Manufacturer :	LogicEnergy
Type / Model No. :	LeWL
Serial No. :	489/O716
Assigned equipment no. :	AAST-WL-01
Adjustment :	N/A
Remark :	Received with good condition

**2. Customer information**

Customer :	Castco Testing Centre Limited
Address :	33, On Kui Street, Fanling, N.T.
Date of receipt :	24 September 2020

**3. Date of performance of the calibration**

Date of calibration :	30 September 2020
-----------------------	-------------------

Approved Signatory

Warren Yeung

Company Chop:

Certificate issue date: 5 October 2020



- The certificate shall not reproduced except in full without the written approval of CAL LAB LTD
- The certificate is issued subject to the latest Term and Condition, available assessable at our web site

CT-BEG-02  
Page 1 of 3  
cc0092010

Cal Lab Limited  
Address: Room 2103, Technology Plaza, 29-35 Sha Tsui Road, Tsuen Wan, NT, Hong Kong  
Tel : (852)25680106 Fax(852)30116194 Email: info@callab.com.hk Website:callab.com.hk



**4. Result of Calibration**

**a) Wind Speed**

Reference reading ; m/s	Measured reading ; m/s	Error of indication ; %
0.0	0.00	N/A
5.0	4.90	-2.0
10.0	9.88	-1.2
15.0	14.85	-1.0

Estimated expanded uncertainty: 0.5 m/s      Technical Requirement: +/-5% or 1 m/s

**b) Wind direction**

Reference reading	Measured reading	Error of indication
0°	0°	0°
45°	45°	0°
90°	90°	0°
135°	135°	0°
180°	180°	0°
225°	225°	0°
270°	270°	0°
315°	315°	0°

Estimated expanded uncertainty: 5°      Technical Requirement: N/A

- The certificate shall not reproduced except in full without the written approval of CAL LAB LTD
- The certificate is issued subject to the latest Term and Condition, available assessable at our web site

Page 2 of 3  
cc0092010

Cal Lab Limited  
Address: Room 2103, Technology Plaza, 29-35 Sha Tsui Road, Tsuen Wan, NT, Hong Kong  
Tel : (852)25680106 Fax(852)30116194 Email: info@callab.com.hk Website:callab.com.hk

## Calibration Certificate of Wing Logger



### 5. Reference method for calibration

Wind Speed	SOP-251
Wind Direction	SOP-252

### 6. Environment condition of calibration

Temperature ; °C	24.0 °C
Relative humidity ; %RH	55 %RH

### 7. Reference equipment used in the calibration

Item	Model	Serial No.	Expiry date	Traceable to
Reference anemometer	405-V1	41543692	1 Jan 2021	SMQ

- Note1: The estimated expanded uncertainties have been calculated in "Evaluation and expression of uncertainty in measurement" and give an internal estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.
- Note2: The standard (s) and instrument used in the calibration are traceable to national or international recognized standard and are calibrated on a schedule to maintain the accuracy and good condition.
- Note3: The result reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.
- Note4: The result shows in this calibration certificate relate only to the item calibrated, and the result only applies to the calibration item as received.

\*\*\* End of Certificate \*\*\*

CT-END-02

1. The certificate shall not reproduced except in full without the written approval of CAL LAB LTD
2. The certificate is issued subject to the latest Term and Condition, available assessable at our web site

Page 3 of 3  
cc0092010

Cal Lab Limited  
Address: Room 2103, Technology Plaza, 29-35 Sha Tsui Road, Tsuen Wan, NT, Hong Kong  
Tel : (852)25680106 Fax(852)30116194 Email: [info@callab.com.hk](mailto:info@callab.com.hk) Website:[callab.com.hk](http://callab.com.hk)

**Appendix F – Weather information**



## General Information

Date	Absolute Daily Min Temperature (°C)	Absolute Daily Max Temperature (°C)	Total Rainfall (mm)	Mean Relative Humidity (%)
16/02/2021	18.2	24.2	0.0	71
17/02/2021	18.3	24.6	0.0	70
18/02/2021	16.7	22.9	0.0	65
19/02/2021	15.8	22.9	0.0	66
20/02/2021	16.7	23.9	0.0	73
21/02/2021	17.3	24.9	0.0	74
22/02/2021	18.4	26.0	0.0	78
23/02/2021	18.8	26.4	0.0	74
24/02/2021	18.9	22.9	Trace	79
25/02/2021	18.8	22.7	1.8	85
26/02/2021	20.4	25.1	14.7	86
27/02/2021	18.1	20.8	13.4	89
28/02/2021	18.1	22.8	Trace	83

NOTE1: The above weather information was obtained from manned weather station of Hong Kong Observatory.

NOTE2: Trace means rainfall less than 0.05 mm

<https://www.hko.gov.hk/en/cis/dailyExtract.htm?y=2021&m=2>

## Kai Tak Runway Park Information

Date	Absolute Daily Min Temperature (°C)	Absolute Daily Max Temperature (°C)
16/02/2021	18.2	21.6
17/02/2021	18.0	23.1
18/02/2021	16.1	19.9
19/02/2021	15.8	19.4
20/02/2021	16.3	20.6
21/02/2021	16.2	22.2
22/02/2021	17.3	23.9
23/02/2021	18.5	23.6
24/02/2021	18.6	20.4
25/02/2021	18.7	21.9
26/02/2021	19.7	24.9
27/02/2021	17.7	20.6
28/02/2021	17.9	20.6

NOTE1: The above weather information was obtained from manned weather station of Kai Tak Runway Park.

[https://i-lens.hk/hkweather/history\\_chart.php?date=2021-02-16&chart\\_type=DG\\_TEMP](https://i-lens.hk/hkweather/history_chart.php?date=2021-02-16&chart_type=DG_TEMP)

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
16/02/2021	0:00	0.9	135	17/02/2021	0:00	0.9	67.5	18/02/2021	0:00	0.4	112.5	19/02/2021	0:00	0.9	112.5
16/02/2021	1:00	1.8	45	17/02/2021	1:00	0.9	22.5	18/02/2021	1:00	0.4	135	19/02/2021	1:00	0.4	112.5
16/02/2021	2:00	0.9	33.5	17/02/2021	2:00	0.4	270	18/02/2021	2:00	0.9	135	19/02/2021	2:00	1.3	112.5
16/02/2021	3:00	0.9	90	17/02/2021	3:00	1.3	112.5	18/02/2021	3:00	1.3	112.5	19/02/2021	3:00	1.3	112.5
16/02/2021	4:00	1.3	90	17/02/2021	4:00	2.2	67.5	18/02/2021	4:00	1.3	112.5	19/02/2021	4:00	1.3	112.5
16/02/2021	5:00	2.2	90	17/02/2021	5:00	2.2	112.5	18/02/2021	5:00	1.8	112.5	19/02/2021	5:00	1.8	90
16/02/2021	6:00	1.8	90	17/02/2021	6:00	2.2	112.5	18/02/2021	6:00	1.8	90	19/02/2021	6:00	1.3	112.5
16/02/2021	7:00	3.1	90	17/02/2021	7:00	2.2	90	18/02/2021	7:00	1.3	112.5	19/02/2021	7:00	0.9	90
16/02/2021	8:00	1.9	90	17/02/2021	8:00	2.2	112.5	18/02/2021	8:00	0.9	112.5	19/02/2021	8:00	0.9	112.5
16/02/2021	9:00	0.9	112.5	17/02/2021	9:00	1.3	112.5	18/02/2021	9:00	1.3	90	19/02/2021	9:00	0.4	112.5
16/02/2021	10:00	1.3	112.5	17/02/2021	10:00	0.9	112.5	18/02/2021	10:00	1.3	90	19/02/2021	10:00	0.9	112.5
16/02/2021	11:00	0.9	67.5	17/02/2021	11:00	0.9	112.5	18/02/2021	11:00	0.4	90	19/02/2021	11:00	0.9	90
16/02/2021	12:00	0.4	202.5	17/02/2021	12:00	0.4	112.5	18/02/2021	12:00	0.4	135	19/02/2021	12:00	0.9	112.5
16/02/2021	13:00	0.9	0	17/02/2021	13:00	0.4	112.5	18/02/2021	13:00	0	135	19/02/2021	13:00	0.9	135
16/02/2021	14:00	0.9	90	17/02/2021	14:00	0.4	112.5	18/02/2021	14:00	0	135	19/02/2021	14:00	0.4	112.5
16/02/2021	15:00	0.9	45	17/02/2021	15:00	0.9	90	18/02/2021	15:00	0	112.5	19/02/2021	15:00	0.4	135
16/02/2021	16:00	0.4	157.5	17/02/2021	16:00	0.4	112.5	18/02/2021	16:00	0.4	112.5	19/02/2021	16:00	0	112.5
16/02/2021	17:00	0.9	292.5	17/02/2021	17:00	0.4	112.5	18/02/2021	17:00	0.4	112.5	19/02/2021	17:00	0.4	135
16/02/2021	18:00	1.3	22.5	17/02/2021	18:00	0	112.5	18/02/2021	18:00	0	112.5	19/02/2021	18:00	0.4	135
16/02/2021	19:00	1.3	45	17/02/2021	19:00	0.4	112.5	18/02/2021	19:00	0	112.5	19/02/2021	19:00	0	135
16/02/2021	20:00	0.9	67.5	17/02/2021	20:00	0.4	45	18/02/2021	20:00	0.4	112.5	19/02/2021	20:00	0.4	112.5
16/02/2021	21:00	0.9	22.5	17/02/2021	21:00	0.4	135	18/02/2021	21:00	0	112.5	19/02/2021	21:00	0	135
16/02/2021	22:00	0.9	112.5	17/02/2021	22:00	0	135	18/02/2021	22:00	0	112.5	19/02/2021	22:00	0	135
16/02/2021	23:00	0.4	112.5	17/02/2021	23:00	0.4	135	18/02/2021	23:00	0.4	112.5	19/02/2021	23:00	0.4	135

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
20/02/2021	0:00	0	135	21/02/2021	0:00	0	67.5	22/02/2021	0:00	1.8	90	23/02/2021	0:00	0.9	112.5
20/02/2021	1:00	0.4	135	21/02/2021	1:00	0.4	67.5	22/02/2021	1:00	1.8	67.5	23/02/2021	1:00	0.9	45
20/02/2021	2:00	0.4	247.5	21/02/2021	2:00	0.9	112.5	22/02/2021	2:00	1.8	67.5	23/02/2021	2:00	1.3	337.5
20/02/2021	3:00	0.4	112.5	21/02/2021	3:00	1.3	112.5	22/02/2021	3:00	1.8	90	23/02/2021	3:00	0.9	292.5
20/02/2021	4:00	0.4	135	21/02/2021	4:00	1.8	90	22/02/2021	4:00	2.7	90	23/02/2021	4:00	1.3	112.5
20/02/2021	5:00	1.3	90	21/02/2021	5:00	2.2	112.5	22/02/2021	5:00	1.3	45	23/02/2021	5:00	0.9	90
20/02/2021	6:00	1.3	90	21/02/2021	6:00	1.8	112.5	22/02/2021	6:00	1.3	157.5	23/02/2021	6:00	1.3	112.5
20/02/2021	7:00	1.3	112.5	21/02/2021	7:00	1.8	90	22/02/2021	7:00	0.9	112.5	23/02/2021	7:00	1.8	112.5
20/02/2021	8:00	0.4	112.5	21/02/2021	8:00	0.9	112.5	22/02/2021	8:00	0.9	247.5	23/02/2021	8:00	1.3	112.5
20/02/2021	9:00	0.4	112.5	21/02/2021	9:00	0.9	45	22/02/2021	9:00	1.3	112.5	23/02/2021	9:00	0.9	90
20/02/2021	10:00	0	180	21/02/2021	10:00	0.9	135	22/02/2021	10:00	0.9	45	23/02/2021	10:00	0.9	112.5
20/02/2021	11:00	0.4	180	21/02/2021	11:00	0.9	270	22/02/2021	11:00	0.9	22.5	23/02/2021	11:00	1.8	112.5
20/02/2021	12:00	0.9	112.5	21/02/2021	12:00	0.4	135	22/02/2021	12:00	0.9	90	23/02/2021	12:00	0.9	112.5
20/02/2021	13:00	0	112.5	21/02/2021	13:00	0.4	225	22/02/2021	13:00	0.4	247.5	23/02/2021	13:00	0.9	112.5
20/02/2021	14:00	0.4	112.5	21/02/2021	14:00	1.8	112.5	22/02/2021	14:00	0.9	112.5	23/02/2021	14:00	0.9	135
20/02/2021	15:00	0.9	112.5	21/02/2021	15:00	2.2	0	22/02/2021	15:00	1.3	67.5	23/02/2021	15:00	0.9	112.5
20/02/2021	16:00	0	112.5	21/02/2021	16:00	2.2	67.5	22/02/2021	16:00	0.9	180	23/02/2021	16:00	0.4	112.5
20/02/2021	17:00	0	90	21/02/2021	17:00	2.7	90	22/02/2021	17:00	1.3	45	23/02/2021	17:00	0.4	90
20/02/2021	18:00	0	112.5	21/02/2021	18:00	2.7	67.5	22/02/2021	18:00	1.8	45	23/02/2021	18:00	0.4	90
20/02/2021	19:00	0	112.5	21/02/2021	19:00	3.1	90	22/02/2021	19:00	1.3	22.5	23/02/2021	19:00	0	135
20/02/2021	20:00	0	90	21/02/2021	20:00	1.8	67.5	22/02/2021	20:00	1.3	45	23/02/2021	20:00	0.9	90
20/02/2021	21:00	0.4	112.5	21/02/2021	21:00	3.1	67.5	22/02/2021	21:00	1.3	67.5	23/02/2021	21:00	0.9	112.5
20/02/2021	22:00	0	112.5	21/02/2021	22:00	2.7	45	22/02/2021	22:00	0.4	0	23/02/2021	22:00	0	112.5
20/02/2021	23:00	0	112.5	21/02/2021	23:00	2.7	90	22/02/2021	23:00	0.9	45	23/02/2021	23:00	0.4	112.5

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
24/02/2021	0:00	0.9	112.5	25/02/2021	0:00	1.8	112.5	26/02/2021	0:00	2.7	90	27/02/2021	0:00	0.9	135
24/02/2021	1:00	0.4	112.5	25/02/2021	1:00	0.9	337.5	26/02/2021	1:00	2.2	67.5	27/02/2021	1:00	1.3	135
24/02/2021	2:00	0.4	135	25/02/2021	2:00	0.9	135	26/02/2021	2:00	2.2	45	27/02/2021	2:00	1.3	90
24/02/2021	3:00	0.4	135	25/02/2021	3:00	0.9	247.5	26/02/2021	3:00	2.7	90	27/02/2021	3:00	1.3	112.5
24/02/2021	4:00	1.3	112.5	25/02/2021	4:00	0.9	22.5	26/02/2021	4:00	1.8	45	27/02/2021	4:00	1.3	112.5
24/02/2021	5:00	0.9	135	25/02/2021	5:00	1.3	112.5	26/02/2021	5:00	1.8	90	27/02/2021	5:00	0.9	112.5
24/02/2021	6:00	1.3	112.5	25/02/2021	6:00	0.9	67.5	26/02/2021	6:00	1.8	67.5	27/02/2021	6:00	0.9	112.5
24/02/2021	7:00	0.4	90	25/02/2021	7:00	0.9	90	26/02/2021	7:00	1.3	45	27/02/2021	7:00	0.9	112.5
24/02/2021	8:00	0.4	112.5	25/02/2021	8:00	0.9	45	26/02/2021	8:00	1.3	67.5	27/02/2021	8:00	1.3	112.5
24/02/2021	9:00	1.3	112.5	25/02/2021	9:00	0.9	337.5	26/02/2021	9:00	0.9	45	27/02/2021	9:00	1.3	90
24/02/2021	10:00	1.8	112.5	25/02/2021	10:00	0.4	112.5	26/02/2021	10:00	1.3	0	27/02/2021	10:00	1.3	90
24/02/2021	11:00	0.9	112.5	25/02/2021	11:00	0.9	292.5	26/02/2021	11:00	0.4	135	27/02/2021	11:00	0.9	112.5
24/02/2021	12:00	0.9	112.5	25/02/2021	12:00	0.9	157.5	26/02/2021	12:00	1.3	90	27/02/2021	12:00	0.9	90
24/02/2021	13:00	0.9	247.5	25/02/2021	13:00	0.9	67.5	26/02/2021	13:00	0.4	90	27/02/2021	13:00	1.3	112.5
24/02/2021	14:00	0	157.5	25/02/2021	14:00	1.8	22.5	26/02/2021	14:00	1.3	112.5	27/02/2021	14:00	0.9	112.5
24/02/2021	15:00	0	157.5	25/02/2021	15:00	1.3	337.5	26/02/2021	15:00	0.9	135	27/02/2021	15:00	0	112.5
24/02/2021	16:00	0	247.5	25/02/2021	16:00	1.3	45	26/02/2021	16:00	0.9	45	27/02/2021	16:00	0	90
24/02/2021	17:00	0.4	270	25/02/2021	17:00	1.3	45	26/02/2021	17:00	0.4	90	27/02/2021	17:00	0.4	202.5
24/02/2021	18:00	0	292.5	25/02/2021	18:00	0.4	270	26/02/2021	18:00	0.9	135	27/02/2021	18:00	0	202.5
24/02/2021	19:00	0.4	337.5	25/02/2021	19:00	1.3	135	26/02/2021	19:00	0.4	22.5	27/02/2021	19:00	0	202.5
24/02/2021	20:00	0.4	112.5	25/02/2021	20:00	1.3	90	26/02/2021	20:00	0.4	112.5	27/02/2021	20:00	0.9	135
24/02/2021	21:00	0.4	112.5	25/02/2021	21:00	2.2	45	26/02/2021	21:00	0.9	112.5	27/02/2021	21:00	0.9	0
24/02/2021	22:00	0.4	22.5	25/02/2021	22:00	1.8	67.5	26/02/2021	22:00	0.9	112.5	27/02/2021	22:00	1.3	0
24/02/2021	23:00	1.3	112.5	25/02/2021	23:00	0.9	112.5	26/02/2021	23:00	0.9	90	27/02/2021	23:00	1.3	135

Mean Wind Speed and Wind Direction recorded by the weather station setup at the rooftop of Ng Wah Catholic Secondary School

Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction	Date	Time	Wind Speed (m/s)	Wind Direction
28/02/2021	0:00	1.3	90												
28/02/2021	1:00	0.4	180												
28/02/2021	2:00	1.3	90												
28/02/2021	3:00	1.3	247.5												
28/02/2021	4:00	1.3	90												
28/02/2021	5:00	0.9	225												
28/02/2021	6:00	2.2	112.5												
28/02/2021	7:00	1.3	45												
28/02/2021	8:00	1.3	337.5												
28/02/2021	9:00	2.2	67.5												
28/02/2021	10:00	2.7	67.5												
28/02/2021	11:00	2.7	0												
28/02/2021	12:00	2.7	90												
28/02/2021	13:00	2.7	67.5												
28/02/2021	14:00	3.6	45												
28/02/2021	15:00	4	67.5												
28/02/2021	16:00	4.5	90												
28/02/2021	17:00	2.2	67.5												
28/02/2021	18:00	2.7	90												
28/02/2021	19:00	2.2	45												
28/02/2021	20:00	1.8	67.5												
28/02/2021	21:00	1.3	45												
28/02/2021	22:00	1.8	90												
28/02/2021	23:00	2.2	112.5												

# **Appendix G – 24-hr TSP monitoring results and graphical presentation**





Location: AM2(A) – Ng Wah Catholic Secondary School

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
17/02/2021	Sunny	19.0	1019.5	15.7207	15.8569	0.1362	5097.7	5121.72	1441	50	50	1.51	2183	62
23/02/2021	Sunny	25.7	1015	18.1954	18.4162	0.2208	5121.85	5145.86	1441	50	50	1.49	2142	103
													Maximum	103
													Minimum	62
													Average	83
													Action Level	175
													Limit Level	260

Location: AM3 – Sky Tower

Start Date	Weather	Air Temp. (°C)	Atmospheric Pressure (hPa)	Filter weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (min)	Flow Rate (cfm)		Av. Flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
17/02/2021	Sunny	19.0	1019.5	15.8123	15.933	0.1207	2546.47	2570.52	1443	50	50	1.46	2100	57
23/02/2021	Sunny	25.7	1015	15.8419	16.0428	0.2009	2571.37	2595.39	1441	50	50	1.42	2047	98
													Maximum	98
													Minimum	57
													Average	78
													Action Level	172
													Limit Level	260

## 24-hour average TSP

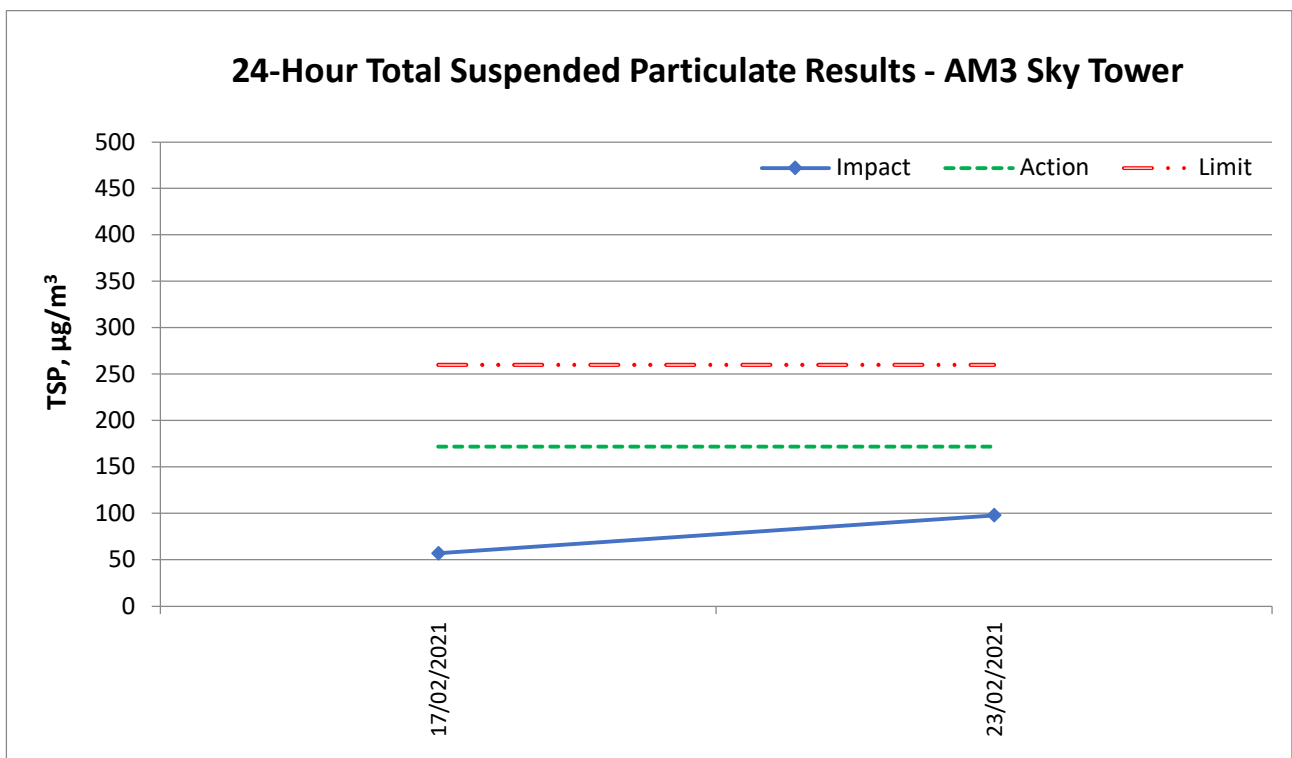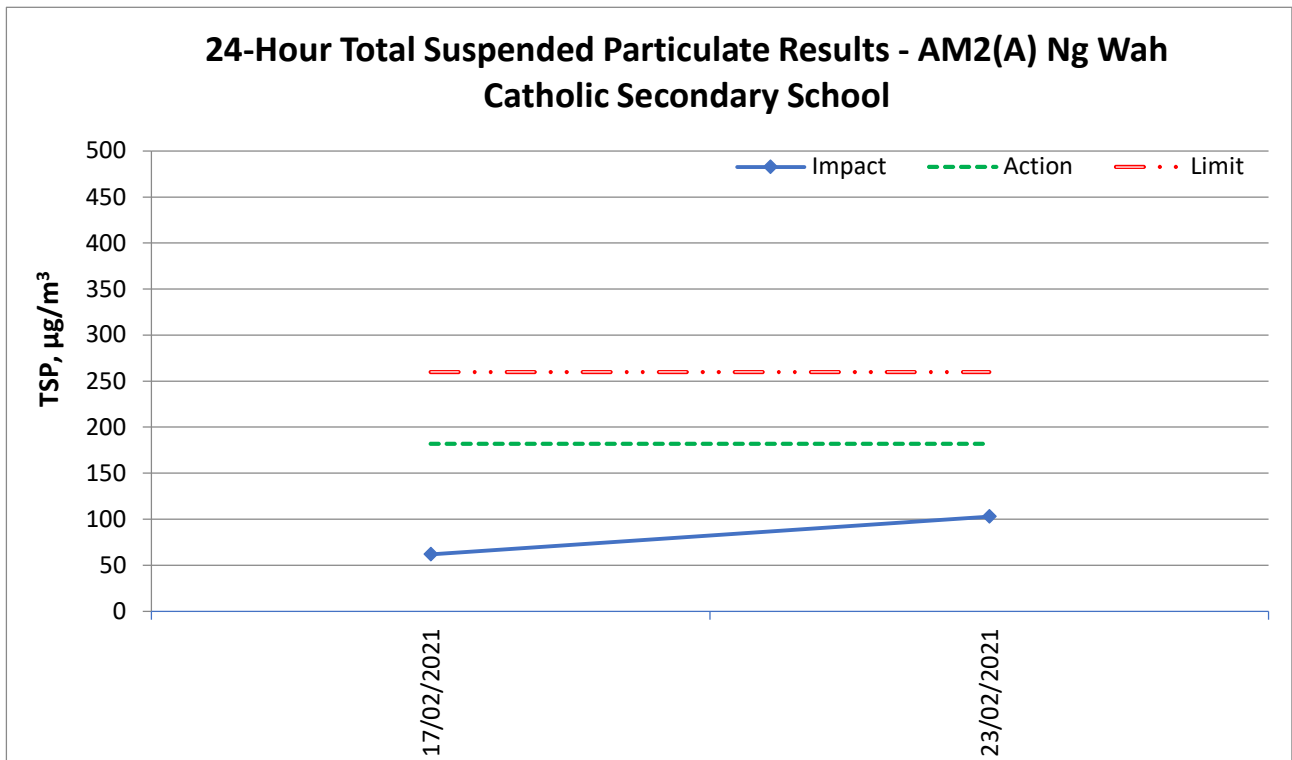

**Appendix H – 1-hr TSP monitoring results and graphical presentation**

Location:  
**AM2(A) –  
 Ng Wah Catholic  
 Secondary School**



Date	Measurement Period			1-hr TSP concentration, $\mu\text{g}/\text{m}^3$	Weather
17/2/2021	13:00	-	14:00	48	Sunny
	14:00	-	15:00	53	
	15:00	-	16:00	50	
23/2/2021	9:00	-	10:00	51	Sunny
	10:00	-	11:00	47	
	11:00	-	12:00	48	
Maximum				53	
Minimum				47	
Average				50	
Action Level				302	
Limit Level				500	

Location:  
**AM3 -  
 Sky Tower**

Date	Measurement Period			1-hr TSP concentration, $\mu\text{g}/\text{m}^3$	Weather
17/2/2021	9:00	-	10:00	33	Sunny
	10:00	-	11:00	34	
	11:00	-	12:00	37	
23/2/2021	13:00	-	14:00	35	Sunny
	14:00	-	15:00	38	
	15:00	-	16:00	42	
Maximum				42	
Minimum				33	
Average				37	
Action Level				301	
Limit Level				500	

c

# 1-hour average TSP

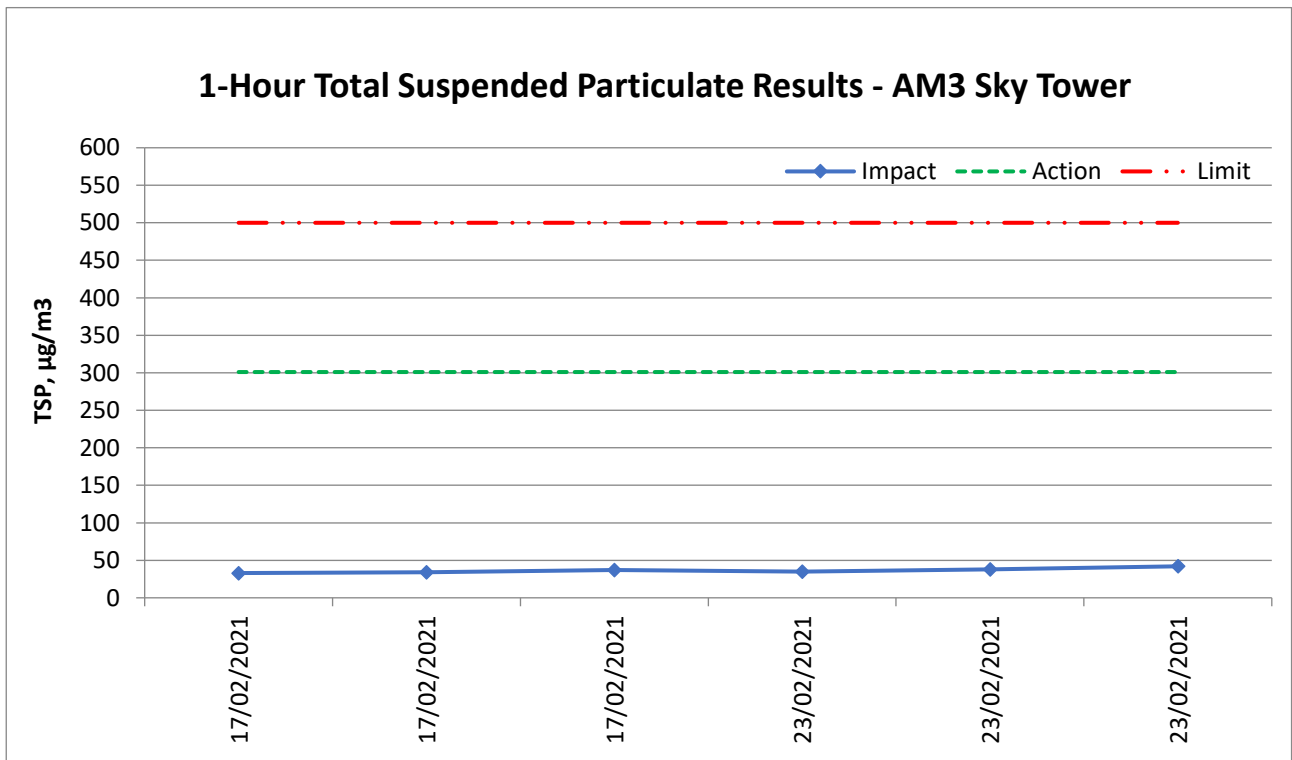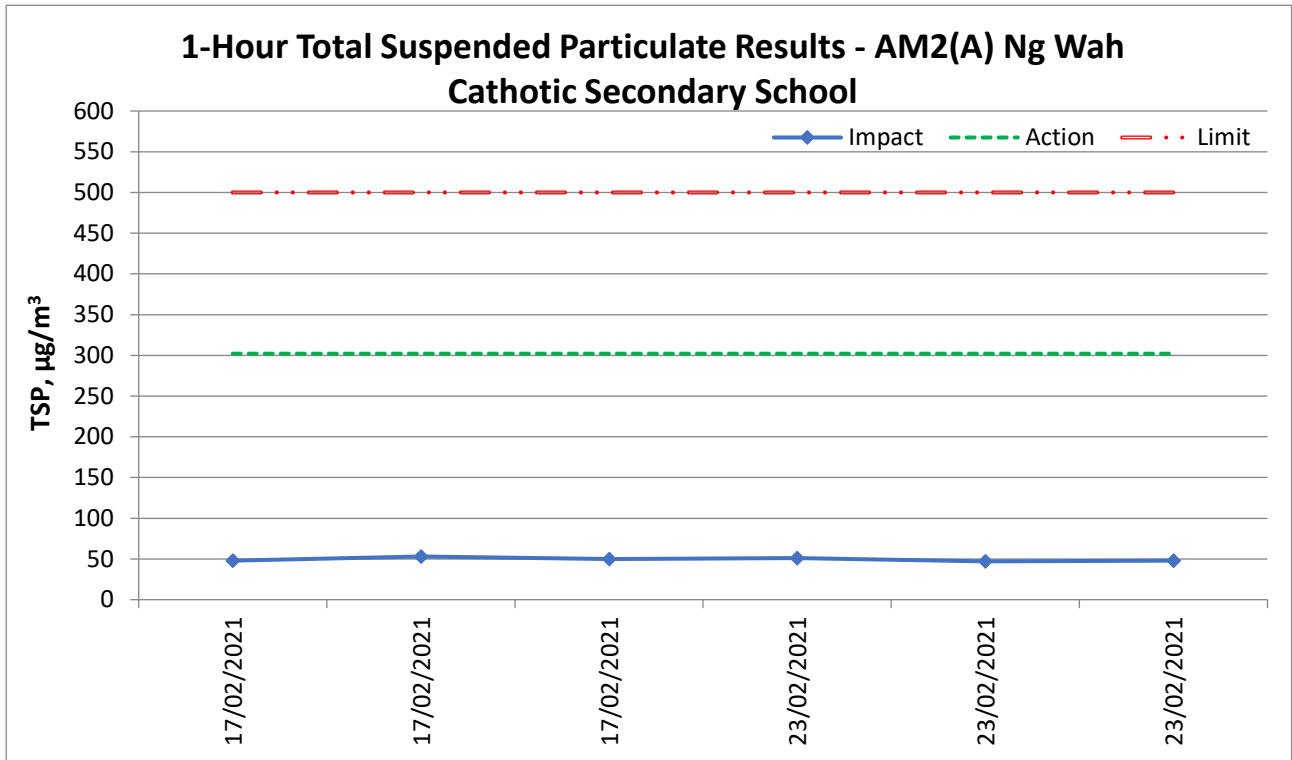

**Appendix I – Event and Action Plan for air quality**



Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contractor, IEC and Supervisor /ER;</li> <li>3. Repeat measurement to confirm finding.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Action Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contractor, IEC and Supervisor /ER;</li> <li>3. Increase monitoring frequency to daily;</li> <li>4. Discuss with IEC and Contractor on remedial actions required;</li> <li>5. Assess the effectiveness of Contractor's remedial actions;</li> <li>6. If exceedance continues, arrange meeting with IEC and Supervisor /ER;</li> <li>7. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the Supervisor /ER on the effectiveness of the proposed remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise implementation of remedial measures;</li> <li>5. Conduct meeting with ET and IEC if exceedance continues.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET and IEC on proper remedial actions;</li> <li>2. Submit proposals for remedial actions to Supervisor /ER and IEC within three working day of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Amend proposal if appropriate.</li> </ol>
Limit Level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contractor, IEC, Supervisor /ER, and EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Assess effectiveness of</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss possible remedial measures with ET and Contractor;</li> <li>4. Advise the Supervisor /ER</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Discuss with ET and IEC on proper remedial actions;</li> <li>3. Submit proposal for remedial actions to Supervisor /ER and IEC</li> </ol>

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results.	on the effectiveness of the proposed remedial measures.	4. Implemented; Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues.	within three working days of notification; 4. Implement the agreed proposals.
Limit Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Notify IEC, Supervisor /ER, Contractor and EPD;</li> <li>2. Repeat measurement to confirm findings;</li> <li>3. Carry out analysis of Contractor's working procedures to identify source and investigate the causes of exceedance;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Arrange meeting with IEC, Supervisor /ER and Contractor to discuss the remedial action to be taken;</li> <li>6. Assess effectiveness of Contractor's remedial actions and keep EPD, IEC and Supervisor /ER informed of the results;</li> <li>7. If exceedance stop, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with Supervisor /ER, ET, and Contractor on the potential remedial actions;</li> <li>4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Discuss with ET and IEC on proper remedial actions;</li> <li>3. Submit proposal for remedial actions to Supervisor /ER and IEC within three working days of notification;</li> <li>4. Implement the agreed proposals;</li> <li>5. Submit further remedial actions if problem still not under control;</li> <li>6. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated.</li> </ol>

**Appendix J – Calibration certificates, catalogue of noise monitoring equipment**



# Calibration Certificate of Sound Level Meter



**中国赛宝实验室计量检测中心**  
(工业和信息化部电子第五研究所计量检测中心)  
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

## 校准证书 CALIBRATION CERTIFICATE

证书编号: 2HB20001172-0003  
Certificate No.



委托单位: Client	Castco Testing Centre Limited		
仪器名称: Description	Sound Level Meter		
型号规格: Model/Type	NL-52		
制造商: Manufacturer	RION		
机身号: Serial No.	00976203		
管理号: Asset No.	AAST-SLM-10		
接收日期: Rec. Date	2020-07-15	校准日期: Cal. Date	2020-07-20
签发日期: App. Date	2020-07-20	建议校准周期: Reference Cal. Period	12个月(12 Months)
结论: Conclusion	所校准项目合格(Passed at Calibration Items)		

校准:  
Calibrated by

签发:  
Approved by

核验:  
Inspected by

印章:  
Stamp

赛宝计量检测中心  
广州总部地址: 广州天河区东圃庄路110号  
客服电话: 020-87237633 传真: 020-87236189  
投诉电话: 020-87236896  
邮件: cal@ceprei.com  
网址: www.ceprei-cal.com

CEPREI Calibration and Testing Centre  
H.Q. Addr: No.110.Dongguzhuang Road,Tianhe District,Guangzhou  
Service Tel: 020-87237633 Fax: 020-87236189  
Complaint Tel: 020-87236896  
Email: cal@ceprei.com  
Website: www.ceprei-cal.com

证书编号(Certificate No.): 2HB20001172-0003

## 说明 DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025的要求, 获得中国合格评定国家认可委员会(CNAS)认可, 认可证书号为: CNAS L13344。  
This laboratory quality management system meets the ISO/IEC 17025 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.

2. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):  
\* JJG 188-2017 声级计检定规程: Sound pressure level: (20~130)dB; Frequency Weighting: (20~130)dB@B(10 Hz~20kHz).  
\* 详细内容请查看CNAS网站中注册编号为L13344的证书附件, 超出范围的内容未被认可。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited).

3. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):

名称 (Description)	证书号/有效期/溯源单位 (Certificate No./Due Date/Traceability to)	技术指标 (Specification)
数字多用表	4GC19040017-0001/2020-11-03/赛宝	DCV: $\pm 0.0035\%$ ; ACV: $\pm 0.06\%$ ; DCI: $\pm 0.05\%$ ; ACI: $\pm 0.1\%$ ; R: $\pm 0.01\%$ ; f: $\pm 0.01\%$
步进衰减器	4GC20000158-0012/2021-04-29/赛宝	$\pm 3dB$
标准传声器	GFJGJL1001200310164/2021-02-26/航空304所	$U=(0.05-0.12)dB (k=2)$
声校准器	4GC19040146-0209/2020-12-29/赛宝	1级
正弦信号发生器	4GC19040057-0001/2020-11-05/赛宝	f: $\pm 1mHz$ ; 失真度: $< -70dB$
PULSE分析系统	4GC20000009-0001/2021-01-08/赛宝	频率: $U_{rel}=0.001\%$ ; $k=2$ ; 电压: $U_{rel}=0.04\%$ ; $k=2$
前置放大器	GFJGJL1001200310165/2021-02-26/航空304所	$U=0.3dB (k=2)$

4. 校准地点(The calibration place):  
广州市天河区东莞庄路110号401楼振动声学室

5. 环境条件(Environmental conditions):  
温度(Temperature): 24°C 相对湿度(Relative Humidity): 60%

6. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定, 由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。  
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.

7. 证书中"P"、"合格"代表"测量结果在允许范围内", "F"、"不合格"代表"测量结果不在允许范围内", "N/A"代表"不适用"。本证书报告的判定规则和结论仅供参考, 使用人员应结合实际测量的要求合理使用, 如考虑测量结果测量不确定度的影响等。  
"P" and "Pass" in this certificate stand for "Low Limit: the measured value  $\leq$  High Limit", "F" and "Fail" stand for "the measured value  $<$  Low Limit or the measured value  $>$  High Limit", "N/A" stands for "Not Applicable". The judgment rules and conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.

8. 建议校准周期是本实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议, 供委托方参考。委托方可以根据实际使用情况自行决定样品的建议校准周期。  
The reference calibration period is based on the reference documents and normal operating conditions of the calibrated instrument. It is only for reference. The client may decide the calibration period of the instrument according to the actual use.

注: 1. 本证书未经本机构书面授权, 不得部分复制。(The certificate shall not be partly reproduced without written approval of the laboratory.)

2. 本次校准结果仅与被校物有关。(The results are only related to the items calibrated.)



# Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB20001172-0003

**1 外观与工作正常性检查 (Appearance and Function Check)**

无影响证书中校准结果准确度的因素和缺陷。

There are no factor and defect that affect the calibration result accuracy of the certificate.

**2 指示声级调整 (Indication SPL Calibration)**

频率(Frequency)=1000Hz

传声器型号 (Microphone Type)	传声器编号 (Microphone SN.)	放大器型号 (Preamplifier Type)	放大器编号 (Preamplifier SN.)
UC-59	12132	NH-25	76320

声校准器型号 (Calibrator Type)	标准声压级 (Reference SPL) (dB)	校准前示值 (Before Calibration) (dB)	校准后示值 (After Calibration) (dB)	U (k=2) (dB)
4231	94.0	94.0	94.0	0.2

**3 级线性 (Level Linearity)**

**3.1 参考级量程 (Reference Range)**

频率(Frequency): 8000Hz

起始点指示声级(Sound Level Indication of Start Point):	90.0 dB
起始点以上间隔10dB点的最大误差(Maximum Error for each 10dB above Start Point):	-0.2 dB
U (k=2)	0.6 dB
上限以下5dB间隔1dB点的最大误差(Maximum Error for each 1dB below Upper Limit 5dB):	-0.2 dB
U (k=2)	0.6 dB
起始点以下间隔10dB点的最大误差(Maximum Error for each 10dB below Start Point):	-0.2 dB
U (k=2)	0.6 dB
下限以上5dB间隔1dB点的最大误差(Maximum Error for each 1dB above Lower Limit 5dB):	-0.2 dB
U (k=2)	0.6 dB

**3.2 其它级量程 (Other Range)**

频率(Frequency): 1000Hz

起始点指示声级(Sound Level Indication of Start Point):	90.0 dB
起始点以上间隔10dB点的最大误差(Maximum Error for each 10dB above Start Point):	-0.2 dB
U (k=2)	0.4 dB
上限以下5dB间隔1dB点的最大误差(Maximum Error for each 1dB below Upper Limit 5dB):	-0.2 dB
U (k=2)	0.4 dB
起始点以下间隔10dB点的最大误差(Maximum Error for each 10dB below Start Point):	-0.2 dB
U (k=2)	0.4 dB
下限以上5dB间隔1dB点的最大误差(Maximum Error for each 1dB above Lower Limit 5dB):	-0.1 dB
U (k=2)	0.4 dB

数据页(Data sheet) ID: U071288

第 5 页,共 8 页  
Page of



证书编号(Certificate No.): 2HB20001172-0003

**4 A计权特性(A-Weighting Characteristic)**

频率 (Frequency) (Hz)	实测值 (Actual) (dB)	理论值 (Theoretical value) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
20	-50.7	-50.5	-0.2	±2.0	P	0.5
25	-45.0	-44.7	-0.3	+2.0 ~ -1.5	P	0.5
31.5	-39.5	-39.4	-0.1	±1.5	P	0.5
40	-34.5	-34.6	0.1	±1.0	P	0.5
50	-30.2	-30.2	0.0	±1.0	P	0.5
63	-26.1	-26.2	0.1	±1.0	P	0.5
80	-22.4	-22.5	0.1	±1.0	P	0.5
100	-19.1	-19.1	0.0	±1.0	P	0.5
125	-16.1	-16.1	0.0	±1.0	P	0.5
160	-13.2	-13.4	0.2	±1.0	P	0.5
200	-10.8	-10.9	0.1	±1.0	P	0.5
250	-8.6	-8.6	0.0	±1.0	P	0.5
315	-6.6	-6.6	0.0	±1.0	P	0.4
400	-4.7	-4.8	0.1	±1.0	P	0.4
500	-3.2	-3.2	0.0	±1.0	P	0.4
630	-1.8	-1.9	0.1	±1.0	P	0.4
800	-0.8	-0.8	0.0	±1.0	P	0.4
1000(Ref)	0.0	0.0	0.0	±0.7	P	0.4
1250	0.6	0.6	0.0	±1.0	P	0.6
1600	0.9	1.0	-0.1	±1.0	P	0.6
2000	1.1	1.2	-0.1	±1.0	P	0.6
2500	1.1	1.3	-0.2	±1.0	P	0.6
3150	1.0	1.2	-0.2	±1.0	P	0.6
4000	0.7	1.0	-0.3	±1.0	P	0.6
5000	0.3	0.5	-0.2	±1.5	P	0.6
6300	-0.2	-0.1	-0.1	+1.5 ~ -2.0	P	0.6
8000	-1.1	-1.1	0.0	+1.5 ~ -2.5	P	0.6
10000	-2.3	-2.5	0.2	+2.0 ~ -3.0	P	0.6
12500	-4.3	-4.3	0.0	+2.0 ~ -5.0	P	1.0
16000	-8.5	-6.6	-1.9	+2.5 ~ -16.0	P	1.0
20000	-18.4	-9.3	-9.1	+3.0 ~ -∞	P	1.0

第 6 页,共 8 页  
Page of

数据页(Data sheet) ID: U071288



## Calibration Certificate of Sound Level Meter



证书编号(Certificate No.): 2HB20001172-0003

### 5 C计权特性(C-Weighting Characteristic)

频率 (Frequency) (Hz)	实测值 (Actual) (dB)	理论值 (Theoretical value) (dB)	误差 (Error) (dB)	允许误差 (Limit) (dB)	结论 (Pass/Fail) (P/F)	U (k=2) (dB)
20	-6.6	-6.2	-0.4	±2.0	P	0.5
25	-4.6	-4.4	-0.2	+2.0 ~ -1.5	P	0.5
31.5	-3.1	-3.0	-0.1	±1.5	P	0.5
40	-1.9	-2.0	0.1	±1.0	P	0.5
50	-1.3	-1.3	0.0	±1.0	P	0.5
63	-0.8	-0.8	0.0	±1.0	P	0.5
80	-0.4	-0.5	0.1	±1.0	P	0.5
100	-0.2	-0.3	0.1	±1.0	P	0.5
125	-0.1	-0.2	0.1	±1.0	P	0.5
160	0.0	-0.1	0.1	±1.0	P	0.5
200	0.0	0.0	0.0	±1.0	P	0.5
250	0.1	0.0	0.1	±1.0	P	0.5
315	0.1	0.0	0.1	±1.0	P	0.4
400	0.1	0.0	0.1	±1.0	P	0.4
500	0.1	0.0	0.1	±1.0	P	0.4
630	0.1	0.0	0.1	±1.0	P	0.4
800	0.1	0.0	0.1	±1.0	P	0.4
1000(Ref.)	0.0	0.0	0.0	±0.7	P	0.4
1250	-0.1	0.0	-0.1	±1.0	P	0.6
1600	-0.2	-0.1	-0.1	±1.0	P	0.6
2000	-0.3	-0.2	-0.1	±1.0	P	0.6
2500	-0.5	-0.3	-0.2	±1.0	P	0.6
3150	-0.7	-0.5	-0.2	±1.0	P	0.6
4000	-1.1	-0.8	-0.3	±1.0	P	0.6
5000	-1.5	-1.3	-0.2	±1.5	P	0.6
6300	-2.1	-2.0	-0.1	+1.5 ~ -2.0	P	0.6
8000	-3.0	-3.0	0.0	+1.5 ~ -2.5	P	0.6
10000	-4.2	-4.4	0.2	+2.0 ~ -3.0	P	0.6
12500	-6.2	-6.2	0.0	+2.0 ~ -5.0	P	1.0
16000	-10.4	-8.5	-1.9	+2.5 ~ -16.0	P	1.0
20000	-20.4	-11.2	-9.2	+3.0 ~ ∞	P	1.0

数据页(Data sheet) ID: U071288

第 7 页,共 8 页  
Page of



证书编号(Certificate No.): 2HB20001172-0003

### 6 自生噪声 (Autogenous noise)

计权 (Weighting)	实测值 (Actual) (dB)
A	24.0

以下空白/No data hereafter



第 8 页,共 8 页  
Page of

数据页(Data sheet) ID: U071288

## Catalogue of Sound Calibrator

### For microphone calibration NC-74

#### How to use

Carefully insert the microphone all the way into the coupler of the NC-74. Then simply turn the power on to apply a constant sound pressure level to the diaphragm of the microphone.




Usage example (NL series)

The performance of the NC-74 is suitable for calibration of high-precision sound level meters. The unit is compact, lightweight, and easy to use. Two IEC LR6 (size AA) alkaline batteries will power the unit for more than 30 hours of continuous use at room temperature.

#### Atmospheric pressure compensation principle

The NC-74 incorporates a sensor that detects atmospheric pressure. Based on the information provided by the sensor, the CPU controls the signal amplitude. This allows the unit to always provide the correct output for achieving constant sound pressure level, regardless of fluctuations in atmospheric pressure.

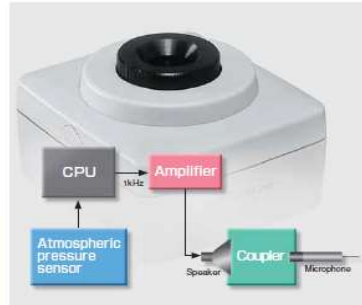

#### Using the 1/2-inch adapter

To allow calibration of sound level meter microphones with 1 inch diameter, the 1/2-inch microphone adapter can be removed. 1/2-inch microphones are calibrated with the adapter in place.



#### Specifications

Applicable standards	IEC 60642:2003 Class 1 JIS C 1615:2004 Class 1	
Suitable microphones	1-inch microphones	IEC 61094-1 Type L81P UC-27 UC-28 UC-34
	1/2-inch microphones	IEC 61094-1 Type L82aP UC-59 UC-57 UC-60A UC-60 UC-26 UC-30 UC-31 UC-33P
Nominal sound pressure level	94 dB	
Sound pressure level tolerance	±1.0 dB	
Nominal frequency	1 kHz	
Frequency tolerance	±1.0 % or less	
Power requirements	IEC LR6 (size AA) alkaline battery × 2	
Dimensions, mass	Approx. 49 (W) × 80 (D) × 74 (H) mm Approx. 206 g (including batteries)	
Supplied accessories	Case × 1 IEC LR6 (size AA) alkaline battery × 2 1/2-inch microphone adapter NC-74-002 × 1	

\* Specification subject to change without notice.

**RION CO., LTD.**

3-20-41, Higashinomachi, Kokubunji, Tokyo 185-8533, Japan  
Tel: +81-42-359-7888 Fax: +81-42-359-7442  
<http://www.rion.co.jp/english/>

Distributed by:



Printed in Japan 0510-1 0807.P.MP



ISO 14001 RION CO., LTD.  
ISO 9001 RION CO., LTD.

## Calibration Certificate of Sound Calibrator



中国赛宝实验室计量检测中心  
(工业和信息化部电子第五研究所计量检测中心)  
CHINA CEPREI LABORATORY CALIBRATION & TESTING CENTRE

## 校准证书 CALIBRATION CERTIFICATE

证书编号: ZHH20001561-0002

Certificate No.



委托单位: Client	Custoo Testing Centre Limited	
仪器名称: Description	Sound Level Calibrator	
型号规格: Model/Type	NC-74	
制造商: Manufacturer	RION	
机身号: Serial No.	34678556	
管理号: Asset No.	AAST-SLC-06	
接收日期: Rec. Date	2020-09-08	校准日期: Cal. Date
签发日期: App. Date	2020-09-12	建议校准周期: Reference Cal. Period
结论: Conclusion	所校准项目合格(Passed at Calibration Items)	

CEPREI

校准:  
Calibrated by

陈卓辉

核验:  
Inspected by

钟淑

签发:  
Approved by

郑木力

印章:  
Stamp

赛宝计量检测中心  
广州总部地址: 广州天河区东圃镇林村119号  
客服电话: 020-87277032 传真: 020-87256169  
投诉电话: 020-87238896  
邮件: cal@cppei.com  
网址: www.ccppei-cal.com

CEPREI Calibration and Testing Centre  
E.Q. AAA No.118,Dongyuanhuang Road,Tianhe District,Guangzhou  
Service Tel: 020-87277032 Fax: 020-87236169  
Complaint Tel: 020-87238896  
Email: cal@cppei.com  
Website: www.ccppei-cal.com

第 1 页, 共 5 页  
Page of

# Calibration Certificate of Sound Calibrator

证书编号(Certificate No.): ZHBJ20091561-0002

## 说 明 DIRECTIONS

1. 本机构质量管理体系符合ISO/IEC 17025:2017标准的要求，获得中国合格评定国家认可委员会（CNAS）认可，认可证书号为：CNAS L13344。  
This laboratory quality management system meets the ISO/IEC 17025:2017 and is accredited by the China National Accreditation Service for Conformity Assessment, No. CNAS L13344.
2. 本次校准的技术依据及CNAS认可范围(Reference documents and CNAS accredited scopes):  
\* JG 176-2005 声校准器检定规程; Sound Pressure Level: 94dB, 104dB, 114dB, 124dB(315Hz~3kHz); 94dB, 104dB, 114dB,(1.5Hz~10kHz); Frequency: 31.5Hz~16kHz; Harmonic Distortion: 0~10%, (20Hz~20 kHz).  
\* 请参看本证书CNAS认可证书编号为L13344的证书附件，超出范围的内容未获认可。(Please see the attachment of certificate No. L13344 at CNAS website for details, beyond which is not accredited).
3. 本次校准所使用的主要测量标准(The main measurement standards used during the calibration):  

名称 (Description)	证书号/有效日期/溯源单位 (Certificate No./Date/Traceability to)	技术指标 (Specification)	测量范围 (Measuring Range)
PULSE分析系统	L1566/2020-02/91/2021-04-26/中国计量院	频率:( $L_{\text{ref}}=0.01\%$ ), $L_{\text{ref}}=1$ ;电压: $L_{\text{ref}}=0.04\%$ , $L_{\text{ref}}=2$	频率:从50Hz~31.26kHz 电压:1V~10V
标准扬声器	GFJCL100120010164/2021-02-26/航空304所	$L_{\text{ref}}=0.05-0.12\text{dB}$ (A=2)	20Hz~20kHz
前置放大器	GFJCL1001200510165/2021-02-26/航空304所	$C=0.3\text{dB}$ (A=2)	(10~20000) Hz
4. 校准地点(The calibration place):  
广州市天河区东莞庄路110号401楼振动声学室
5. 环境条件(Environmental conditions):  
温度(Temperature): 24°C 相对湿度(Relative Humidity): 60%
6. 本证书中给出的扩展不确定度依据JJF1059.1-2012《测量不确定度的评定与表示》评定，由合成标准不确定度乘以包含概率约为95%时对应的包含因子k得到。  
The extended uncertainty given in this certificate is evaluated according to JJF1059.1-2012 "Evaluation and Expression of Uncertainty in Measurement", and is calculated by multiplying the combined standard uncertainty by the coverage factor k which corresponding to the coverage probability about 95%.
7. 证书中“P”、“合格”代表“测量结果在允许范围内”，“F”、“不合格”代表“测量结果不在允许范围内”，“N/A”代表“不适用”。本证书报告的判定规则和结论仅供参考，使用人员应结合实际测量的要求合理使用，如考虑测量结果测量不确定度的影响等。  
“P” and “Pass” in this certificate stand for “Low Limit: the measured value > High Limit”, “F” and “Fail” stand for “the measured value < Low Limit or the measured value > High Limit”, “N/A” stands for “Not Applicable”. The judgment rules and conclusions of this certificate are for reference only. Users should use them reasonably according to the actual measurement requirements, such as considering the impact of measurement uncertainty, etc.
8. 建议校准周期基本实验室依据本证书报告的技术依据和仪器设备常规使用条件给出的建议，供委托方参考。委托方可以根据实际使用情况自行决定样品的建议校准周期。  
The reference calibration period is based on the reference documents and normal operating conditions of the calibrated instrument. It is only for reference. The client may decide the calibration period of the instrument according to the actual use.

注: 1. 本证书未经本机构书面授权，不得部分复制。(The certificate shall not be partly reproduced without written approval of the laboratory.)

2. 本次校准结果仅与被校物有关。(The results are only related to the items calibrated.)

第 3 页, 共 5 页  
Page 3 of 5



证书编号(Certificate No.): ZHBJ20091561-0002

### 1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中校准结果准确性的因素和缺陷。

There are no factor and defect that affect the calibration result accuracy of the certificate.

### 2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	允许范围 (Limit)	结论 (Pass/Fail)	U (dB)
94	94.05	0.05	≤0.40	P	0.10

### 3 频率 (Frequency)

规定频率 (Prescribed Freq.)	测量频率 (Measured Freq.)	频率误差的绝对值 (Absolute value of Freq.)	允许范围 (Limit)	结论 (Pass/Fail)	U (%)
1000	1003.7	0.37	≤1.00	P	0.10

### 4 总失真 (Distortion)

规定声压级 (Prescribed SPL)	规定频率 (Measured Freq.)	总失真 (Distortion)	允许范围 (Limit)	结论 (Pass/Fail)	U (%)
94	1000	0.96	≤3.00	P	3.0

11 个字符的条形码

# CEPREI

数据页(Data sheet) ID: U013103

第 5 页, 共 5 页  
Page 5 of 5



# Calibration Certificate of Sound Calibrator



证书编号(Certificate No.): 2HB20001172-0006

## 1 外观与工作正常性检查 (Appearance and Function Check)

无影响证书中校准结果准确度的因素和缺陷。

There are no factor and defect that affect the calibration result accuracy of the certificate.

## 2 声压级 (Sound Pressure Level)

规定声压级 (Prescribed SPL)	测量声压级 (Measured SPL)	声压级差的绝对值 (Absolute value of SPL)	允许范围 (Limit)	结论 (Pass/Fail)	$U$ (k=2)
(dB)	(dB)	(dB)	(dB)	(Pass/Fail)	(dB)
94	94.38	0.38	≤0.40	P	0.10

## 3 频率 (Frequency)

规定频率 (Prescribed Fre.)	测量频率 (Measured Fre.)	频率误差的绝对值 (Absolute value of Fre.)	允许范围 (Limit)	结论 (Pass/Fail)	$U_{rel}$ (k=2)
(Hz)	(Hz)	(%)	(%)	(Pass/Fail)	(%)
1000	1002.0	0.20	≤1.00	P	0.10

## 4 总失真 (Distortion)

规定声压级 (Prescribed SPL)	规定频率 (Measured Fre.)	总失真 (Distortion)	允许范围 (Limit)	结论 (Pass/Fail)	$U_{rel}$ (k=2)
(dB)	(Hz)	(%)	(%)	(Pass/Fail)	(%)
94	1000	2.48	≤3.00	P	5.0

以下空白/No data hereafter

CEPREI

数据页(Data sheet) ID: U013393

第 5 页,共 5 页  
Page of

# Catalogue of Air Flow Meter (TSI TA440)

## SPECIFICATIONS

THERMAL ANEMOMETERS  
MODELS TA410, TA430 AND TA440

### Velocity

Range (TA410)	0 to 20 m/s (0 to 4,000 ft/min)
Range (TA430, TA440)	0 to 30 m/s (0 to 6,000 ft/min)
Accuracy (TA410) <sup>1,2</sup>	±5% of reading or ±0.025 m/s (±5 ft/min), whichever is greater
Accuracy (TA430, TA440) <sup>1,2</sup>	±3% of reading or ±0.015 m/s (±3 ft/min), whichever is greater
Resolution	0.01 m/s (1 ft/min)

### Duct Size (TA430, TA440)

Dimensions	1 to 635 cm in increments of 0.1 cm (1 to 250 inches in increments of 0.1 in.)
------------	--

### Volumetric Flow Rate (TA430, TA440)

Range	Actual range is a function of velocity, and duct size
-------	---

### Temperature

Range (TA410, TA430)	-18 to 93°C (0 to 200°F)
Range (TA440)	-10 to 60°C (14 to 140°F)
Accuracy <sup>3</sup>	±0.3°C (±0.5°F)
Resolution	0.1°C (0.1°F)

### Relative Humidity (TA440 only)

Range	5 to 95% RH
Accuracy <sup>4</sup>	±3% RH
Resolution	0.1% RH

### Wet Bulb Temperature (TA440 only)

Range	5 to 60°C (40 to 140°F)
Resolution	0.1°C (0.1°F)

### Dew Point (TA440 only)

Range	-15 to 49°C (5 to 120°F)
Resolution	0.1°C (0.1°F)

### Instrument Temperature Range

Operating (Electronics)	5 to 45°C (40 to 113°F)
Model TA410, TA430 Operating (Probe)	-18 to 93°C (0 to 200°F)
Model TA440 Operating (Probe)	-10 to 60°C (14 to 140°F)
Storage	-20 to 60°C (-4 to 140°F)

### Data Storage Capabilities (TA430, TA440)

Range	12,700+ samples and 100 test IDs
-------	----------------------------------

### Logging Interval (TA430, TA440)

1 second to 1 hour
--------------------

Specifications subject to change without notice.

TSI and the TSI logo are registered trademarks, and Airflow, the Airflow logo and LogDat2 are trademarks of TSI Incorporated.



Airflow Instruments, TSI Instruments Ltd.  
Visit our website at [www.airflowinstruments.co.uk](http://www.airflowinstruments.co.uk) for more information.

UK Tel: +44 149 4 459200 Germany Tel: +49 241 523030  
France Tel: +33 491 11 87 64

P/N 2980548 Rev D (A4) ©2014 TSI Incorporated

### Time Constant (TA430, TA440)

User selectable

### External Meter Dimensions

8.4 cm x 17.8 cm x 4.4 cm (3.3 in. x 7.0 in. x 1.8 in.)

### Meter Weight with Batteries

0.27 kg (0.6 lbs.)

### Meter Probe Dimensions

Probe Length	101.6 cm (40 in.)
Probe Diameter of Tip	7.0 mm (0.28 in.)
Probe Diameter of Base	13.0 mm (0.51 in.)

### Articulating Probe Dimensions

Articulating Section Length	19.7 cm (7.8 in.)
Diameter of Articulating Knuckle	9.5 mm (0.38 in.)

### Power Requirements

Four AA-size batteries or AC adapter

	TA410	TA430, TA430-A	TA440, TA440-A
Velocity range	+		
0 to 20.00 m/s (0 to 4000 ft/min)			
Velocity range		+	+
0 to 30.00 m/s (0 to 6000 ft/min)			
Temperature	+	+	+
Flow		+	+
Humidity, wet bulb, dew point			+
Probe	Straight	Straight or -A articulated	Straight or -A articulated
Variable time constant		+	+
Manual data logging		+	+
Auto save data logging			+
Statistics		+	+
Review data		+	+
LogDat2 downloading software			+
Free Certificate of Calibration	+	+	+

<sup>1</sup> Temperature compensated over an air temperature range of 5 to 65°C (40 to 150°F).

<sup>2</sup> The accuracy statement begins at 30 ft/min through 4000 ft/min (0.15 m/s through 20 m/s) for the Model TA410, and 30 ft/min through 6,000 ft/min (0.15 m/s through 30 m/s) for Models TA430 and TA440.

<sup>3</sup> Accuracy with instrument case at 25°C (77°F), add uncertainty of 0.03°C (0.05°F/°F) for change in instrument temperature.

<sup>4</sup> Accuracy with probe at 25°C (77°F). Add uncertainty of 0.2% RH/°C (0.1% RH/°F) for change in probe temperature. Includes 1% hysteresis.

# Calibration Certificate of Air Flow Meter



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-Tech Metrology Station



中国认可  
国际互认  
校准  
CALIBRATION  
CNAS L6579

## 校准报告

CALIBRATION REPORT



报告编号: 204202268

第 1 页, 共 3 页  
Page 1 of 3 Pages

客户名称 : Castco Testing Centre Limited

Name of Customer

客户地址 : 33, On Kui Street, Fanling, N.T.

Address of Customer

计量器具名称: 风速仪

Name of Instrument

器具用途 : 环境监测

Use of Instrument

型号/规格 : TA440

Type/Specification

出厂编号 : TA4401232005

Serial No

资产编号 : AAST-FLOW-02

Asset No

制造单位 : TSI

Manufacturer

校准依据 : 参照JJG(建设)0001-1992《热球式风速仪》检定规程校准

Calibrated in Accordance to

(校准专用章)  
Stamp

校准日期 : 2020 年 03 月 16 日

Operation Date

建议复校日期: 2021 年 03 月 15 日

Suggested Recal. Date

签发日期 : 2020 年 03 月 16 日

Issue Date

批准人 : 张正海

Authorized by

签名 :

Signature

核验员 :

Checked by

校准员 :

Calibrated by

校准机构备案号: [2012]粤量校F002号  
地址: 广东省深圳市南山区龙珠大道92号  
电话: 0086-755-26941696 0086-755-26941516  
传真: 0086-755-26941615 0086-755-26941547  
邮编: 518055 网址: www.smq.com.cn  
电子邮件: kfzx@smq.com.cn

Register No.: [2012]粤量校F002号  
Add: No.92, Longzhu Avenue, Nanshan District, Shenzhen, Guangdong, China  
Nanshan District, Shenzhen  
Tel: 0086-755-26941696 0086-755-26941546  
Fax: 0086-755-26941615 0086-755-26941547  
Post Code: 518055 http://www.smq.com.cn  
E-mail: kfzx@smq.com.cn



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-Tech Metrology Station

## 校准报告

CALIBRATION REPORT

报告编号: 204202268  
Report No

第 2 页, 共 3 页  
Page 2 of 3 Pages

### 校准用主要计量标准装置信息 Main Standard Devices Used

名称 Equipment Name	测量范围 Measuring Range	不确定度/准确度等级/ 最大允许误差 Uncertainty/Accuracy Class/ Maximum Permissible Error	计量标准考核证书号 Certificate No	有效期至 Due Date

### 校准用主要标准器信息 Main Standards of Measurement Used

名称 Equipment Name	测量范围 Measuring Range	不确定度/准确度等级/ 最大允许误差 Uncertainty/Accuracy Class/ Maximum Permissible Error	设备编号 Equipment No	证书号/溯源单位 Certificate No/ Traceability to	有效期至 Due Date
皮托静压管	—	$\pm 1.002 \text{ k}=1.001$	SB4562/01	GQJ(V) LT2015-0028号/中国计量院	2020-05-05
风洞			SB4562	NSS201901168/广东省计量院	2024-06-26
数字压力计			SB10930	RGpv2019-2205/中国计量院	2020-09-26

### 附加说明 Appended Directions

委托日期: 2020 年 03 月 10 日  
Application Date  
校准地点: 本院104室  
Operation Location  
环境条件: 温度 21.3 °C 相对湿度 60 %  
Operation Environment  
符合性及限制使用说明: 参照校准结果使用  
Statement of Compliance and Limitation



# Calibration Certificate of Air Flow Meter



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-tech Metrology Station

## 校准报告 CALIBRATION REPORT

报告编号: 204202268  
Report No

第 3 页, 共 3 页  
Page 3 of 3 Pages

### 校准结果 Results of Calibration

零位: 0.00m/s      满度: ---

风速示值:

序号	标准风速 (m/s)	仪器指示读数 (m/s)	修正值 (m/s)
1	0.40	0.38	+0.02
2	1.00	0.95	+0.05
3	2.00	1.70	+0.30
4	5.00	4.30	+0.70
5	10.00	9.70	+0.30
6	15.00	14.89	+0.11
7	20.00	20.23	-0.23

附加说明:

1. 大气压力: 1018.0hPa
2. 依据JJF1059.1-2012测量不确定度评定与表示, 测量结果的扩展不确定度:  $U_{95}=3.0\%$ ,  $k=2$

以 下 空 白



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-tech Metrology Station



## 校准报告 CALIBRATION REPORT



报告编号: 204202267

第 1 页, 共 3 页  
Page 1 of 3 Pages

客户名称 : Castco Testing Centre Limited  
Name of Customer  
客户地址 : 33, On Kui Street, Fanling, N.T.  
Address of Customer  
计量器具名称: 风速仪  
Name of Instrument  
器具用途 : 环境监测  
Use of Instrument  
型号/规格 : TA440  
Type/Specification  
出厂编号 : TA4401706003  
Serial No  
资产编号 : AAST-FLOW-03  
Asset No  
制造单位 : TSI  
Manufacturer  
校准依据 : 参照JJG (建设) 0001-1992《热球式风速仪》检定规程校准  
Calibrated in Accordance to

(校准专用章)  
Stamp

校准日期 : 2020 年 03 月 16 日  
Operation Date Year Month Day

建议复校日期: 2021 年 03 月 15 日  
Suggested Recal.Date Year Month Day

签发日期 : 2020 年 03 月 16 日  
Issue Date Year Month Day

批准人 : 张正海  
Authorized by

签名 : 张正海  
Signature

核验员 : 于飞  
Checked by

校准员 : 张嘉琪  
Calibrated by

校准机构备案号: [2012]粤量校F002号  
地址: 广东省深圳市南山区龙珠大道92号  
电话: 0086-755-26941696 0086-755-26941546  
传真: 0086-755-26941615 0086-755-26941547  
邮编: 518055 网址: www.saq.com.cn  
电子邮箱: kfzx@saq.com.cn

Register No.: [2012]粤量校F002号  
Add: No.92, Longzhu Avenue, Nanshan District, Shenzhen, Guangdong, China  
Nanshan District, Shenzhen  
Tel: 0086-755-26941696 0086-755-26941546  
Fax: 0086-755-26941615 0086-755-26941547  
Post Code: 518055 http://www.saq.com.cn  
E-mail: kfzx@saq.com.cn



# Calibration Certificate of Air Flow Meter



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-tech Metrology Station

## 校准报告

CALIBRATION REPORT

报告编号: 204202267  
Report No

第 2 页, 共 3 页  
Page 2 of 3 Pages

### 校准用主要计量标准装置信息

Main Standard Devices Used

名称	测量范围	不确定度/准确度等级/ 最大允许误差	计量标准考核证书号	有效期至
Equipment Name	Measuring Range	Uncertainty/Accuracy Class/ Maximum Permissible Error	Certificate No	Due Date

### 校准用主要标准器信息

Main Standards of Measurement Used

名称	测量范围	不确定度/准确度等级/ 最大允许误差	设备编号	证书号/溯源单位	有效期至
Equipment Name	Measuring Range	Uncertainty/Accuracy Class/ Maximum Permissible Error	Equipment No	Certificate No/ Traceability to	Due Date
应托静压管	---	$\pm 1.002 \quad k=1.001$	SB4562/01	GQJ (V) LT2015-0028号/中国计量院	2020-05-05
风洞	---	---	SB4562	NSS201901168/广东省计量院	2024-06-26
数字压力计	---	---	SR10930	RCpv2019-2205/中国计量院	2020-09-26

### 附加说明

Appended Directions

委托日期: 2020年03月10日  
Application Date  
校准地点: 本院104室  
Operation Location  
环境条件: 温度 21.3 °C 相对湿度 60 %  
Operation Environment  
符合性及限制使用说明: 参照校准结果使用  
Statement of Compliance and Limitation



深圳市计量质量检测研究院  
Shenzhen Academy of Metrology & Quality Inspection  
国家高新技术计量站  
National Hi-tech Metrology Station

## 校准报告

CALIBRATION REPORT

报告编号: 204202267  
Report No

第 3 页, 共 3 页  
Page 3 of 3 Pages

### 校准结果

Results of Calibration

零位: 0.00m/s      满度: ---

风速示值:

序号	标准风速 (m/s)	仪器指示读数 (m/s)	修正值 (m/s)
1	0.40	0.38	+0.02
2	1.00	0.93	+0.07
3	2.00	1.90	+0.10
4	5.00	4.75	+0.25
5	10.00	9.90	+0.10
6	15.00	15.06	-0.06
7	20.00	20.18	-0.18

附加说明:

1. 大气压力: 1018.0hPa
2. 依据JJF1059.1-2012测量不确定度评定与表示, 测量结果的扩展不确定度:  $U_{95}=3.0\%$ ,  $k=2$



以 下 空 白

**Appendix K – Noise monitoring results and graphical presentation**


**M4(A) – Le Billionnaire**

Date	Temp (°C)	Weather	Measured Noise Level at M11, dB(A)							Limit
			Time		Baseline	L <sub>Aeq</sub>	L <sub>A10</sub>	L <sub>A90</sub>		
17/02/2021	19.0	Sunny	9:38	-	10:08	69.5	69.2	70.4	67.3	75
23/02/2021	25.7	Sunny	13:08	-	13:38	69.5	69.0	69.8	67.1	75
							Maximum	69.2		
							Minimum	69.0		
							Average	69.1		


**M5(A) – Prince Ritz**

Date	Temp (°C)	Weather	Measured Noise Level at M12, dB(A)							Limit
			Time		Baseline	L <sub>Aeq</sub>	L <sub>A10</sub>	L <sub>A90</sub>		
17/02/2021	19.0	Sunny	10:36	-	11:06	72.5	73.2	74.8	71.0	75
23/02/2021	25.7	Sunny	14:05	-	14:35	72.5	70.0	71.0	68.8	75
							Maximum	73.2		
							Minimum	70.0		
							Average	71.9		

**L<sub>Aeq</sub>, 30-min graphical results of M4(A) – Le Billionnaire**

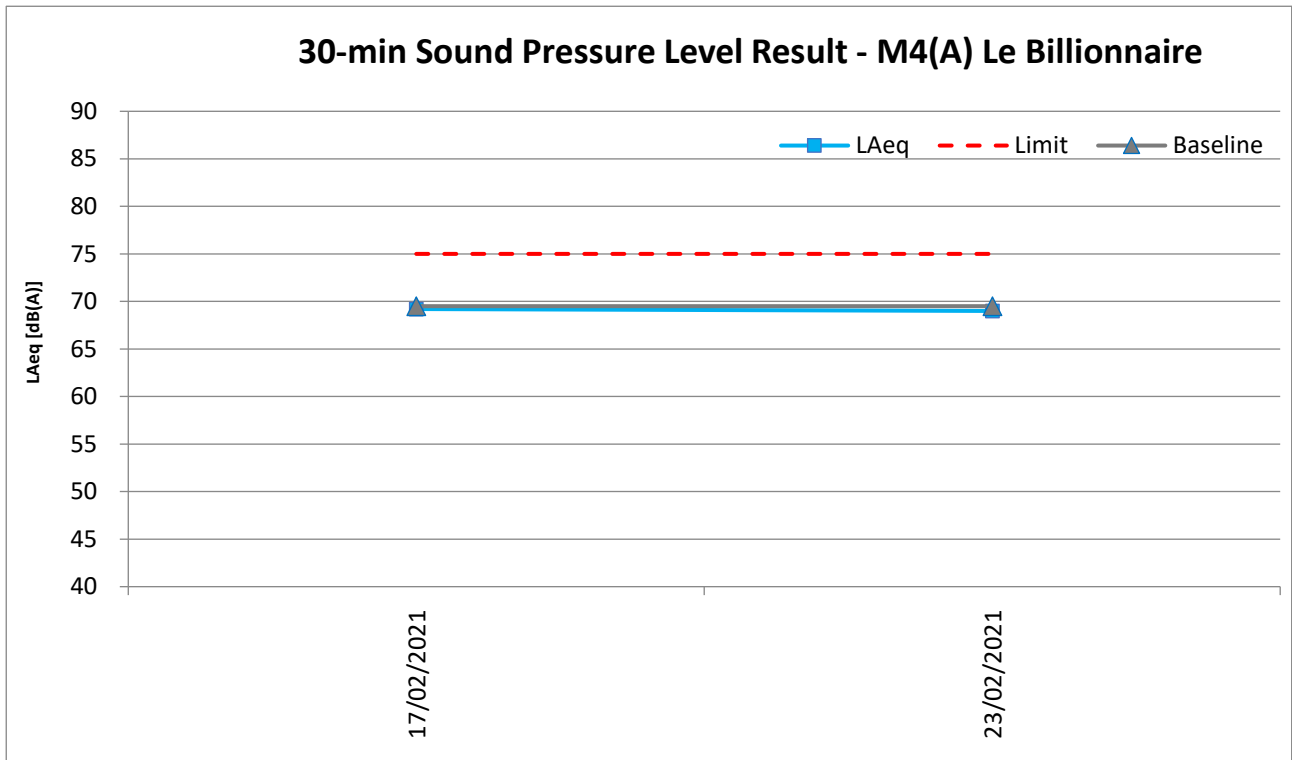

**L<sub>Aeq</sub>, 30-min graphical results of M5(A) – Prince Ritz**

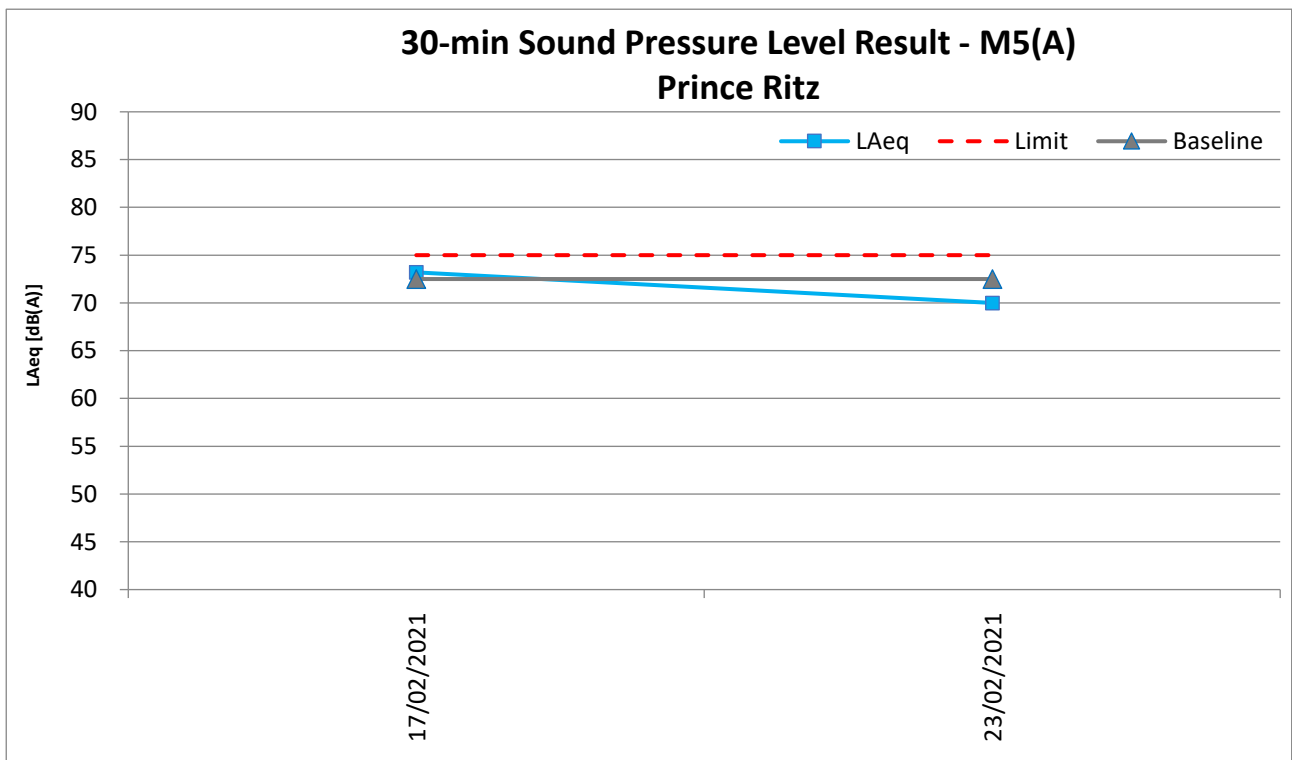

**Appendix L – Event and Action Plan for noise**

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Action Level being exceeded	<ol style="list-style-type: none"> <li>1. Notify Supervisor / ER, IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, Supervisor / ER and Contractor;</li> <li>4. Discuss with the IEC and Contractor on remedial measures required;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness.</li> </ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> <li>1. Review the investigation results submitted by the ET;</li> <li>2. Review the proposed remedial measures submitted by the Contractor and advise the ER accordingly;</li> <li>3. Advise the Supervisor / ER on the proposed remedial measures.</li> </ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures.</li> </ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposal to IEC and Supervisor / ER;</li> <li>2. Implement noise mitigation proposals.</li> </ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>
Limit Level being exceeded	<ol style="list-style-type: none"> <li>1. Inform IEC, Supervisor /ER, Contractor and EPD;</li> <li>2. Repeat measurement to confirm findings;</li> <li>3. Increase monitoring frequency;</li> <li>4. Identify source and investigate the cause of exceedance;</li> <li>5. Carry out analysis of Contract's working procedure;</li> <li>6. Discuss remedial measures required with the IEC, Contractor and Supervisor /ER;</li> <li>7. Assess effectiveness of</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss the potential remedial actions with Supervisor /ER, ET and Contractor;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Supervisor /ER accordingly.</li> </ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC and Supervisor /ER within 3 working days of notification;</li> <li>3. Implement the agreed proposal;</li> <li>4. Submit further proposal if problem still not under control;</li> <li>5. Stop the relevant portion of works as instructed by the Supervisor /ER until the exceedance is abated.</li> </ol> <p>(The above actions should be</p>

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
	<p>Contractor's remedial actions and keep IEC, EPD, and Supervisor /ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified.)</p>		<p>exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<p>taken within 2 working days after the exceedance is identified.)</p>



**Appendix M – Event and Action Plan for Landscape and Visual Impact**

Event	Action			
	ET	IEC	Supervisor / ER	Contractor
Design Check	1. Check final design conforms to the requirements of EP and prepare report.	1. Check report. 2. Recommend remedial design if necessary.	1. Undertake remedial design if necessary.	
Non-conformity on one occasion	1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 4. Monitor remedial actions until rectification has been completed.	1. Check report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Check implementation of remedial measures.	1. Notify Contractor. 2. Ensure remedial measures are properly implemented.	1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.
Repeated Non-conformity	1. Identify Source. 2. Inform IEC and Supervisor /ER. 3. Increase monitoring frequency. 4. Discuss remedial actions with IEC, Supervisor /ER and Contractor. 5. Monitor remedial actions until rectification has been completed. 6. If non-conformity stops, cease additional monitoring.	1. Check monitoring report. 2. Check Contractor's working method. 3. Discuss with ET and Contractor on possible remedial measures. 4. Advise Supervisor /ER on effectiveness of proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Notify Contractor. 2. Ensure remedial measures are properly implemented.	1. Amend working methods. 2. Rectify damage and undertake any necessary replacement.

**Appendix N – Waste Flow Table**

MONTHLY SUMMARY WASTE FLOW TABLE FOR 2021 (YEAR)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Borken Concrete (4)	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Import Fill	Metals	Paper / Cardboard Packaging	Plastics (3)	Chemical Waste	Other, e.g. general refuse
	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000m <sup>3</sup> ]
JAN	0.191597506	0.028739612	0	0	0.162857895	0	0	0	0	0	0.007013333
FEB	0.846959678	0.127043888	0	0	0.719915789	0	0	0	0	0	0.009473333
MAR											
APR											
MAY											
JUNE											
SUB-TOTAL	1.038557184	0.1557835	0	0	0.882773684	0	0	0	0	0	0.016486666
JULY											
AUG											
SEPT											
OCT											
NOV											
DEC											
TOTAL	1.038557184	0.155783500	0	0	0.882773684	0	0	0	0	0	0.016486666

Forecast of Total Quantities of C&D materials to be Generated from the Contracts *										
Total	Borken	Reused in the	Reused in	Disposal as	Import Fill	Metals	Paper /	Plastics (3)	Chemical	Other, e.g.
[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000m <sup>3</sup> ]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000m <sup>3</sup> ]
	3.2			33.652						

- Notes :
- (1) The performance targets are given in PS Clause 25.24.
  - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the site.
  - (3) Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material.
  - \* (4) The summary table shall be submitted to the Project Manager/Supervisor monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.24

# **Appendix O – Environmental Mitigation Implementation Schedule (EMIS)**

**Table 1.1 Implementation Schedule for Air Quality Measures**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.2	8 times daily watering of the work site with active dust emitting activities.	Work site / during construction	Contractor		√			EIAO-TM
S3.2	<p>Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimize cumulative dust impacts.</p> <ul style="list-style-type: none"> <li>- Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.</li> <li>- Misting for the dusty material should be carried out before being loaded into the vehicle.</li> <li>- Any vehicle with an open load carrying area should have properly fitted side and tail boards.</li> <li>- Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.</li> <li>- The tarpaulin should be properly secured and should extend at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation.</li> <li>- The vehicles should be restricted to maximum speed of 10 km per hour and confined haulage and delivery vehicle to designated roadways insider the site. On-site unpaved roads should be compacted and kept free of lose materials.</li> <li>- Vehicle washing facilities should be provided at every vehicle exit point.</li> </ul>	Work site / during construction	Contractor		√			EIAO-TM & Air Quality Objective

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>- The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> <li>- Every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.</li> <li>- Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the three sides; and Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.</li> </ul>							

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning



**Table 1.2 Implementation Schedule for Noise Measures**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.3	Use of quiet PME, movable barriers barrier for Asphalt Paver, Breaker, Excavator and Hand-held breaker and full enclosure for Air Compressor, Bar Bender, Concrete Pump, Generator and Water Pump.	Work Sites / Construction Period	Contractor		✓			EIAO-TM, NCO
S3.3	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>- Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.</li> <li>- Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program.</li> <li>- Mobile plant, if any, should be sited as far away from NSRs as possible.</li> <li>- Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> <li>- Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>- Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	Work Sites / Construction Period	Contractor		✓			EIAO-TM, NCO
S3.3	Scheduling of Construction Works during School Examination Period	Construction site near to school / Examination Period	Contractor		✓			

\* Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

**Table 1.3 Implementation Schedule for Water Quality Measures**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.4	<p><b>Operational Phase</b></p> <p>A surface water drainage system should be provided to collect road runoff. It is recommended that the road drainage should be provided with adequately designed silt trap and oil interceptors, as necessary. The design of the operational stage mitigation measures for the road works shall take into account the guidelines published in ProPECC PN 5/93 "Drainage Plans subject to Comment by the EPD"</p>	Project site / during design and operational stages	CEDD	✓		✓		EIAO-TM, WPCO, ProPECC PN 5/93
S3.4	<p><b>Construction Phase</b></p> <p><u>Construction Runoff</u></p> <p>Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include:</p> <ul style="list-style-type: none"> <li>- use of sediment traps</li> <li>- adequate maintenance of drainage systems to prevent flooding and overflow</li> </ul>	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.4	Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	Work Sites / during construction	Contractor		√			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.	Work Sites / during construction	Contractor		√			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m <sup>3</sup> capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	Work Sites / during construction	Contractor		√			EIAO-TM, WPCO, ProPECC PN 1/94

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.4	Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m <sup>3</sup> should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.4	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	<u>Drainage</u> It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94
S3.4	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.4	All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, ProPECC PN 1/94, WDO
S3.4	<u>Sewage Effluent</u> Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO
S3.4	<u>Stormwater Discharges</u> Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes.	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, TM-DSS
S3.4	<u>Debris and Litter</u> In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur	Work Sites / during construction	Contractor		✓			EIAO-TM, WPCO, WDO

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning



**Table 1.4 Implementation Schedule for Waste Management Measures**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.5	<p>Good Site Practices</p> <p>It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are adhered to. Recommendations for good site practices during construction activities include:</p> <ul style="list-style-type: none"> <li>- Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.</li> <li>- Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>- Provision of sufficient waste disposal points and regular collection for disposal</li> <li>- Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.</li> <li>- A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites)</li> </ul>	Work Sites / during construction	Contractor					EIAO-TM, WDO

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.5	<p>Waste Reduction Measures</p> <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>- Sort C&amp;D waste from demolition of the remaining structures to recover recyclable portions such as metals.</li> <li>- Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>- Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity should be recycled.</li> <li>- Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	Work Sites / during construction	Contractor					EIAO-TM, WDO

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>Construction and Demolition Materials</p> <p>Mitigation measures and good site practices should be incorporated in the contract document to control potential environmental impact from handling and transportation of C&amp;D material. The mitigation measures include:</p> <ul style="list-style-type: none"> <li>- Where it is unavoidable to have transient stockpiles of C&amp;D material within the Project work site pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible.</li> <li>- Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric.</li> <li>- Skip hoist for material transport should be totally enclosed by impervious sheeting.</li> <li>- Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.</li> <li>- The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> <li>- The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.</li> <li>- All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.</li> </ul>	Work sites / during construction	Contractor and Independent Environmental Checker					ETWB TCW No. 33/2002, 31/2004, 19/2005

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>- The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.</p> <p>When delivering inert C&amp;D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&amp;D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Materials" should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.</p>	Work sites / during construction	Contractor and Independent Environmental Checker					ETWB TCW No. 33/2002, 31/2004, 19/2005
S3.5	<p>Chemical Waste</p> <p>After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i>.</p>	Work Sites / during construction	Contractor					<p>Waste Disposal (Chemical Waste) (General) Regulation</p> <p>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</p>

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.5	<p>General Refuse</p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&amp;D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&amp;D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem.</p>	Work Sites / during construction	Contractor					<p>Waste Disposal Ordinance</p> <p>Water Pollution Control Ordinance</p>

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

**Table 1.5 Implementation Schedule for Landscape and Visual Impacts**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.8.12	<p>Construction Phase</p> <ul style="list-style-type: none"> <li>- All existing trees should be carefully protected during construction.</li> <li>- Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.</li> <li>- Control of night-time lighting.</li> <li>- Erection of decorative screen hoarding.</li> </ul>	Works area / During Construction Phase	Contractor	√	√			EIAO-TM
S3.8.13	<p>Operation Phase</p> <ul style="list-style-type: none"> <li>- Compensatory tree planting should be incorporated into the proposed projects where trees are affected.</li> <li>- Tall buffer screen tree / shrub / climber planting should be incorporated to soften hard engineering structures and facilities.</li> <li>- Sensitive streetscape design should be incorporated along all new roads to reflect the new urban development in Kai Tak.</li> <li>- Structure, ornamental tree / shrub / climber planting should be provided along roadside amenity strips and central dividers to enhance the townscape quality, where space is available.</li> <li>- Aesthetically pleasing design as regard to the form, material and finishes should be incorporated to all buildings, engineering structures and associated infrastructure facilities.</li> </ul>	Project area / During Design stage and Operation Phase	CEDD	√		√		EIAO-TM

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

**Appendix P – Summaries of Environmental Complaint, Warning,  
Summon and Notification of Successful Prosecution**



**Reporting Month: February 2021**

<b>Contract No.</b>	<b>Record of Complaint (Yes/No)</b>	<b>Record of Warning (Yes/No)</b>	<b>Notification of Summons and Successful Prosecutions (Yes/No)</b>
ED/2018/05	No	No	No

**Cumulative Statistics on Complaints, Notification of Summons and Successful Prosecutions upto reporting month**

<b>Contract No.</b>	<b>Record of Complaint</b>	<b>Record of Warning</b>	<b>Notification of Summons and Successful Prosecutions</b>
ED/2018/05	0	0	0

<b>Complaint Log for ED/2018/05</b>				
Complaint Ref. No.	Date of Complaint	Description of Complaint	Investigation / Recommendations / Actions	Close-Out Date / Status
