

# Civil Engineering and Development Department

## EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD


Contract No. KL/2010/03  
Kai Tak Development - Stage 2  
infrastructure works at north apron  
area of Kai Tak Airport for residential  
development and government,  
institution or community facilities

Monthly EM&A Report

November 2011

(version 2.0)

Approved By

  
(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

### CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong  
Tel: (852) 2151 2083 Fax: (852) 3107 1388  
Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)

## TABLE OF CONTENTS

<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
Introduction.....	1
Environmental Monitoring Works.....	2
Environmental Licenses and Permits.....	3
Key Information in the Reporting Month .....	3
Future Key Issues.....	3
<b>1. INTRODUCTION.....</b>	<b>4</b>
Background.....	4
Project Organizations.....	4
Construction Activities undertaken during the Reporting Month .....	5
Summary of EM&A Requirements .....	6
<b>2. AIR QUALITY.....</b>	<b>7</b>
Monitoring Requirements .....	7
Monitoring Locations .....	7
Monitoring Equipment.....	7
Monitoring Parameters, Frequency and Duration.....	8
Monitoring Methodology and QA/QC Procedure .....	8
Results and Observations.....	10
<b>3. NOISE .....</b>	<b>13</b>
Monitoring Requirements .....	13
Monitoring Locations .....	13
Monitoring Equipment.....	13
Monitoring Parameters, Frequency and Duration.....	13
Monitoring Methodology and QA/QC Procedures.....	14
Maintenance and Calibration .....	14
Results and Observations.....	15
<b>4. COMPARISON OF EM&amp;A RESULTS WITH EIA PREDICTIONS .....</b>	<b>17</b>
<b>5. LANDSCAPE OF VISUAL.....</b>	<b>19</b>
Monitoring Requirements .....	19
Results and Observations.....	19
<b>6. ENVIRONMENTAL AUDIT.....</b>	<b>20</b>
Site Audits .....	20
Review of Environmental Monitoring Procedures .....	20
Status of Environmental Licensing and Permitting .....	20
Status of Waste Management .....	21
Implementation Status of Environmental Mitigation Measures .....	21
Summary of Mitigation Measures Implemented .....	22
Implementation Status of Event Action Plans .....	22
Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution .....	22
<b>7. FUTURE KEY ISSUES.....</b>	<b>23</b>
Key Issues for the Coming Month .....	23

Monitoring Schedule for the Next Month.....	24
<b>8. CONCLUSIONS AND RECOMMENDATIONS .....</b>	<b>25</b>
Conclusions.....	25
Recommendations.....	25

## **LIST OF TABLES**

Table I	Air Quality and Noise Monitoring Stations for this Project
Table II	Non-compliance Recorded for the Project in the Reporting Month
Table III	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 1.2	Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 2.4	Summary Table of Air Quality Monitoring Results during the reporting month
Table 3.1	Noise Monitoring Stations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Baseline Noise Level and Noise Limit Level for Monitoring Stations
Table 3.5	Summary Table of Noise Monitoring Results during the Reporting Month
Table 4.1	Comparison of 1-hr TSP data with EIA predictions
Table 4.2	Comparison of 24-hr TSP data with EIA predictions
Table 4.3	Comparison of Noise Monitoring Data with EIA predictions
Table 6.1	Summary of Environmental Licensing and Permit Status
Table 6.2	Observations and Recommendations of Site Inspections

## **LIST OF FIGURES**

Figure 1	Layout Plan of the Project Site
Figure 2	Locations of Air Quality Monitoring Stations
Figure 3	Locations of Construction Noise Monitoring Stations
Figure 4	Locations of Wind Anemometer

## **LIST OF APPENDICES**

A	Action and Limit Levels for Air Quality and Noise
B	Copies of Calibration Certificates
C	Weather Information
D	Environmental Monitoring Schedules
E	1-hour TSP Monitoring Results, Graphical Presentations
F	24-hour TSP Monitoring Results, Graphical Presentations
G	Noise Monitoring Results and Graphical Presentations
H	Summary of Exceedance
I	Site Audit Summary
J	Event Action Plans
K	Environmental Mitigation Implementation Schedule (EMIS)
L	Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution
M	Summary of Waste Generation and Disposal Records

## EXECUTIVE SUMMARY

### Introduction

1. This is the 1<sup>st</sup> Monthly Environmental Monitoring and Audit Report prepared by Cinotech Consultants Ltd. for “Contract No. KL/2010/03-Kai Tak Development - Stage 2 infrastructure works at north apron area of Kai Tak Airport for residential development and government, institution or community facilities” (Hereafter referred to as “the Project”). This contract comprises two Schedule 2 designated projects (DPs), namely the new sewage pumping station PS1A serving the planned KTD and the new distributor road D2 serving the planned KTD. The two DPs are part of the designated projects under Environmental Permit No.: EP-344/2009 (“New sewage pumping stations serving Kai Tak Development”) and EP-337/2009 (“New distributor roads serving the planned Kai Tak Development”) respectively. This report documents the findings of EM&A Works conducted in November 2011.
2. With reference to the same principle of EIA report of the Project, air quality monitoring stations within 500m and noise monitoring stations within 300m from the boundary of this Project are considered as relevant monitoring locations. In such regard, the relevant air quality and noise monitoring locations are tabulated in Table I (see Figure 2 and 3 for their locations).

**Table I – Air Quality and Noise Monitoring Stations for this Project**

Locations	Monitoring Stations In accordance with EM&A Manual	Alternative Monitoring Stations
Air Quality Monitoring Stations		
AM1 - Rhythm Garden	No	AM1(A) - Kai Tak Operational Base
AM2 - Lee Kau Yan Memorial School	Yes	N/A
AM6 – Site 1B4 (Planned)	N/A	
Noise Monitoring Stations		
M1 - Buddhist Chi King Primary School	Yes	N/A
M2 - S.K.H. Kowloon Bay Kei Lok Primary School	Yes	N/A
M3 - Cognitio College	Yes	M3(A) - Kai Tak Operational Base
M4 - Lee Kau Yan Memorial School	No	N/A
M9 – Site 1B1 (Planned)	N/A	
M10 – Site 1B4 (Planned)		

3. According to the Environmental Monitoring and Audit Manual (EM&A Manual) of the Kai Tak Development (KTD) Schedule 3 Environmental Impact Assessment (EIA) Report, the impact monitoring at the designated monitoring stations as required in KTD EM&A Manual under two EPs, have been conducted in Contract No. KLN/2010/04 – Environmental Monitoring Works for Kai Tak Development under Schedule 3 of KTD, which is on-going starting from December 2010. The impact monitoring data under Contract No. KLN/2010/04 will be adopted for the Project. Therefore, this report presents the air quality and noise monitoring works extracted from Contract No. KLN/2010/04.
4. The major site activities undertaken in the reporting month included:
- BC6 construction including excavation, steel fixing, formwork erection and concreting;
  - BC3 & 5 construction (excavation and sheet piles cutting for ELS);
  - Hoarding and fencing erection; and
  - Steel piling and dewatering well installation at PS1A.

### Environmental Monitoring Works

5. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Site Inspections/Audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
6. Summary of the non-compliance in the reporting month for the Project is tabulated in Table II.
- Table II Non-compliance Record for the Project in the Reporting Month**

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
1-hr TSP	0	0	N/A
24-hr TSP	0	0	N/A
Noise	0	0	N/A

#### *1-hour & 24-hour TSP Monitoring*

7. All 1-hour & 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### *Construction Noise*

8. All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

### Environmental Licenses and Permits

9. Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Project, Environmental Permits No. EP-344/2009 and EP-337/2009 were issued on 23 April 2009.
10. Registration of Chemical Waste Producer (License: 5213-286-P1079-04).
11. Water Discharge License (License No.: WT00011274-2011 and WT00011276-2011)

### Key Information in the Reporting Month

12. Summary of key information in the reporting month is tabulated in Table III.

**Table III Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Reporting Changes	0	---	N/A	N/A	---
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---

### Future Key Issues

13. The future key environmental issues in the coming month include:
- Dust generation from stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
  - Watering for dust generating activity and on haul road;
  - Proper storage of construction materials on site;
  - Storage of chemicals/fuel and chemical waste/waste oil on site;
  - Accumulation of general and construction waste on site;
  - Noise from operation of the equipment, especially for rock-breaking activities, piling works and machinery on-site;
  - Runoff from exposed slope;
  - Wastewater and runoff discharge from site;
  - Regular removal of silt, mud and sand along u-channels and sedimentation tanks; and
  - Review and implementation of temporary drainage system for the surface runoff.

## 1. INTRODUCTION

### Background

- 1.1 The Kai Tak Development (KTD) is located in the south-eastern part of Kowloon Peninsula, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. It covers a land area of about 328 hectares. Stage 2 infrastructure works at North Apron Area of Kai Tak Airport for Public Housing and Government Office Developments is one of the construction stages of KTD. It contains various Schedule 2 DPs including new distributor roads serving the planned KTD and new sewage pumping stations serving the planned KTD. The general layout of Project 1 and Project 2 is shown in **Figure 1**.
- 1.2 Two Environmental Permits (EPs) No. EP-344/2009 and EP-337/2009 were also issued on 23 April 2009 for new sewage pumping stations serving the planned KTD and new distributor roads serving the planned KTD respectively to Civil Engineering and Development Department as the Permit Holder.
- 1.3 A study of environmental impact assessment (EIA) was undertaken to consider the key issues of air quality, noise, water quality, waste, land contamination, cultural heritage and landscape and visual impact, and identify possible mitigation measures associated with the works. An EIA Report (Register No. AEIAR-130/2009) was approved by the Environmental Protection Department (EPD) on 4 April 2009.
- 1.4 Cinotech Consultants Limited (Cinotech) was commissioned by Peako Engineering Co., Ltd. (the Contractor) to undertake the role of the Environmental Team (ET) for the Contract No. KL/2010/03 - Kai Tak Development – Stage 2 Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities. The construction work under KL/2010/03 comprises the construction of Road D2 & Sewage Pumping Station PS1A which forms a part of the works under two EPs (EP-337/2009 and EP-344/2009).
- 1.5 Cinotech Consultants Limited was commissioned by Peako Engineering Co., Ltd. to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. The construction commencement of this Contract was on 24<sup>th</sup> October 2011 for Sewage Pumping Station PS1A. This is the 1<sup>st</sup> Monthly EM&A report summarizing the EM&A works for the Project in November 2011.

### Project Organizations

- 1.6 Different parties with different levels of involvement in the project organization include:
  - Project Proponent – Civil Engineering and Development Department (CEDD).
  - The Engineer and the Engineer's Representative (ER) – Ove Arup & Partners (ARUP).
  - Environmental Team (ET) – Cinotech Consultants Limited (CCL).
  - Independent Environmental Checker (IEC) – EDMS Consultants Ltd. (EDMS).
  - Contractor – Peako Engineering Co., Ltd. (Peako).



1.7 The key contacts of the Project are shown in Table 1.1.

**Table 1.1 Key Project Contacts**

Party	Role	Contact Person	Position	Phone No.	Fax No.
CEDD	Project Proponent	Mr. Alfred Lee	Engineer	2301 1449	2301 1277
ARUP	Engineer's Representative	Mr. Michael Chan	SRE	2756 8132	2756 8236
		Ms. Gloria Kwok	RE		
Cinotech	Environmental Team	Dr. Priscilla Choy	Environmental Team Leader	2151 2089	3107 1388
		Ms. Ivy Tam	Project Coordinator and Audit Team Leader	2151 2090	
EDMS	Independent Environmental Checker	Mr. Adi Lee	Independent Environmental Checker	2230 7165	3007 8556
Peako	Contractor	Mr. C.P. Lam	Project Manager	27730511	

### Construction Activities undertaken during the Reporting Month

1.8 The site activities undertaken in the reporting month included:

- BC6 construction including excavation, steel fixing, formwork erection and concreting;
- BC3 & 5 construction (excavation and sheet piles cutting for ELS);
- Hoarding and fencing erection; and
- Steel piling and dewatering well installation at PS1A.

1.9 The construction programme showing the inter-relationship with environmental protection/mitigation measures are presented in Table 1.2.

**Table 1.2 Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures**

Construction Works	Major Environmental Impact	Control Measures
As mentioned in Section 1.8	Noise, dust impact, water quality and waste generation	Sufficient watering of the works site with active dust emitting activities Properly cover the stockpiles On-site waste sorting and implementation of trip ticket system Appropriate desilting/sedimentation devices provided on site for treatment before discharge

		Use of quiet plant and well-maintained construction plant Provide movable noise barrier Provide sufficient mitigation measures as recommended in Approved EIA Report/Lease requirement
--	--	--

### Summary of EM&A Requirements

- 1.10 The EM&A programme requires construction noise monitoring, air quality monitoring, landscape and visual monitoring and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
- All monitoring parameters;
  - Action and Limit levels for all environmental parameters;
  - Event Action Plans;
  - Environmental requirements and mitigation measures, as recommended in the EM&A Manual under the two EPs.
- 1.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.
- 1.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely air quality and noise levels and audit works for the Project in November 2011.

## 2. AIR QUALITY

### Monitoring Requirements

- 2.1 According to EM&A Manual under the two EPs, 1-hour and 24-hour TSP monitoring were conducted to monitor the air quality for this Project. For regular impact monitoring, a sampling frequency of at least once in every six days at all of the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days shall be undertaken when the highest dust impact occurs. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

### Monitoring Locations

- 2.2 Three designated monitoring stations were selected for air quality monitoring programme. Impact dust monitoring was conducted at two air quality monitoring stations, namely Kai Tak Operational Base (AM1(A)) and Lee Kau Yan Memorial School (AM2) in the reporting month. Table 2.1 describes the air quality monitoring locations, which are also depicted in **Figure 2**.

**Table 2.1 Locations for Air Quality Monitoring**

Monitoring Stations	Locations	Location of Measurement
AM1(A)	Kai Tak Operational Base	Rooftop (about 9/F) Area
AM2	Lee Kau Yan Memorial School	Rooftop (about 8/F) Area
#AM6	PA 15	Site 1B4 (Planned)

Remarks: # The impact monitoring at these locations will only be carried out until existence of the sensitive receiver at the building.

### Monitoring Equipment

- 2.3 Table 2.2 summarizes the equipment used in the impact air monitoring programme. Copies of calibration certificates are attached in **Appendix B**.

**Table 2.2 Air Quality Monitoring Equipment**

Equipment	Model and Make	Quantity
Calibrator	G25A	1
1-hour TSP Dust Meter	Laser Dust Monitor – Model LD3 & 3B	4
HVS Sampler	GMWS 2310 c/w of TSP sampling inlet	2
Wind Anemometer	Davis Weather Monitor II, Model no. 7440	1

## Monitoring Parameters, Frequency and Duration

- 2.4 Table 2.3 summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period. The air quality monitoring schedule for the reporting month is shown in **Appendix D**.

**Table 2.3 Impact Dust Monitoring Parameters, Frequency and Duration**

Parameters	Frequency
1-hr TSP	Three times / 6 days
24-hr TSP	Once / 6 days

## Monitoring Methodology and QA/QC Procedure

### *1-hour TSP Monitoring*

#### Measuring Procedures

- 2.5 The measuring procedures of the 1-hour dust meters were in accordance with the Manufacturer's Instruction Manual as follows:
- The 1-hour dust meter is placed at least 1.3 meters above ground.
  - Set POWER to "ON" and make sure that the battery level was not flash or in low level.
  - Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
  - Push the knob at MEASURE position.
  - Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
  - Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
  - Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

#### Maintenance/Calibration

- 2.6 The following maintenance/calibration was required for the direct dust meters:
- Check and calibrate the meter by HVS to check the validity and accuracy of the results measured by direct reading method at 2-month intervals throughout all stages of the air quality monitoring.

### *24-hour TSP Monitoring*

#### Instrumentation

- 2.7 High volume (HVS) samplers (Model GMWS-2310 Accu-Vol) completed with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50). Moreover, the HVS also met all the requirements in section 2.5 of the updated EM&A Manual.

#### Operating/Analytical Procedures

- 2.8 Operating/analytical procedures for the operation of HVS were as follows:
- A horizontal platform was provided with appropriate support to secure the samplers against gusty wind.
  - No two samplers were placed less than 2 meters apart.
  - The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
  - A minimum of 2 meters of separation from walls, parapets and penthouses was required for rooftop samples.
  - A minimum of 2 meters separation from any supporting structure, measured horizontally was required.
  - No furnaces or incineration flues were nearby.
  - Airflow around the sampler was unrestricted.
  - The sampler was more than 20 meters from the drip line.
  - Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.
- 2.9 Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 1.1 m<sup>3</sup>/min. and 1.4 m<sup>3</sup>/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.
- 2.10 For TSP sampling, fiberglass filters have a collection efficiency of > 99% for particles of 0.3 µm diameter were used.
- 2.11 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 2.12 The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
- 2.13 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with

swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.

- 2.14 The shelter lid was closed and secured with the aluminum strip.
- 2.15 The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- 2.16 After sampling, the filter was removed and sent to the HOKLAS laboratory (Wellab Ltd.) for weighing. The elapsed time was also recorded.
- 2.17 Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than  $\pm 3^\circ\text{C}$ ; the relative humidity (RH) should be  $< 50\%$  and not vary by more than  $\pm 5\%$ . A convenient working RH is 40%.

#### Maintenance/Calibration

- 2.18 The following maintenance/calibration was required for the HVS:
- The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
  - High volume samplers were calibrated at bi-monthly intervals using G25A Calibration Kit throughout all stages of the air quality monitoring.

#### **Results and Observations**

- 2.19 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 2.20 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 2.21 The air temperature, precipitation and the relative humidity data was obtained from Hong Kong Observatory where the wind speed and wind direction were recorded by the installed Wind Anemometer set at rooftop (about 9/F) of Kai Tak Operational Base. The location is shown in **Figure 4**. This weather information for the reporting month is summarized in **Appendix C**.
- 2.22 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in **Appendices E and F** respectively.
- 2.23 The summary of exceedance record in reporting month is shown in **Appendix H**. No exceedance was recorded for the air quality monitoring.
- 2.24 According to our field observations, the major dust source identified at the designated air

quality monitoring stations are as follows:

Station	Major Dust Source
AM1(A) – Kai Tak Operational Base	Road Traffic Dust Exposed site area and open stockpiles Excavation works Site vehicle movement
AM2 – Lee Kau Yan Memorial School	Road Traffic Dust Exposed site area and open stockpiles Excavation works Site vehicle movement Other construction site (Tung Tau Estate Ph.9) which behind Lee Kau Yan Memorial School

**Table 2.4 Summary Table of Air Quality Monitoring Results during the reporting month**

Parameter	Date	Concentration (µg/m3)	Action Level, µg/m3	Limit Level, µg/m3
AM1(A) – Kai Tak Operational Base				
1-hr TSP	1-Nov-11	147.7	342	500
	1-Nov-11	145.3		
	1-Nov-11	141.4		
	7-Nov-11	118.2		
	7-Nov-11	122.9		
	7-Nov-11	109.1		
	11-Nov-11	121.0		
	11-Nov-11	125.4		
	11-Nov-11	127.9		
	17-Nov-11	169.9		
	17-Nov-11	175.9		
	17-Nov-11	162.5		
	23-Nov-11	122.9		
	23-Nov-11	111.0		
	23-Nov-11	120.6		
	29-Nov-11	79.7		
	29-Nov-11	85.5		
	29-Nov-11	91.4		
24-hr TSP	5-Nov-11	68.1	159	260
	11-Nov-11	86.2		
	17-Nov-11	91.7		
	23-Nov-11	45.8		
	29-Nov-11	23.9		
AM2 – Lee Kau Yan Memorial School				
1-hr TSP	1-Nov-11	140.1	346	500
	1-Nov-11	129.5		
	1-Nov-11	125.2		
	7-Nov-11	104.0		

	7-Nov-11	115.8		
	7-Nov-11	121.7		
	11-Nov-11	120.0		
	11-Nov-11	123.9		
	11-Nov-11	126.6		
	17-Nov-11	153.5		
	17-Nov-11	149.0		
	17-Nov-11	158.2		
	23-Nov-11	147.9		
	23-Nov-11	135.7		
	23-Nov-11	127.2		
	29-Nov-11	137.5		
	29-Nov-11	142.1		
	29-Nov-11	144.5		
24-hr TSP	5-Nov-11	43.4	157	260
	11-Nov-11	98.6		
	17-Nov-11	108.7		
	23-Nov-11	65.0		
	29-Nov-11	76.8		



### 3. NOISE

#### Monitoring Requirements

- 3.1 According to EM&A Manual under the two EPs, construction noise monitoring was conducted to monitor the construction noise arising from the construction activities within KTD. The regular monitoring frequency for each monitoring station shall be on a weekly basis and conduct one set of measurements between 0700 and 1900 hours on normal weekdays. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

#### Monitoring Locations

- 3.2 Six designated monitoring stations were selected for noise monitoring programme. Noise monitoring was conducted at four designated monitoring stations (M1, M2, M3, M4(A)) in the reporting month. **Figure 3** shows the locations of these stations.

**Table 3.1 Noise Monitoring Stations**

Monitoring Stations	Locations	Location of Measurement
M1	Buddhist Chi King Primary School	7/F Sport Area
M2	S.K.H. Kowloon Bay Kei Lok Primary School	7/F Podium
M3(A)	Kai Tak Operational Base	Rooftop (about 9/F) Area
M4	Lee Kau Yan Memorial College	Rooftop (about 7/F) Area
#M9	Site 1B1 (Planned)	-
#M10	Site 1B4 (Planned)	-

Remarks: # The impact monitoring at these locations will only be carried out until existence of the sensitive receiver at the building.

#### Monitoring Equipment

- 3.3 Table 3.2 summarizes the noise monitoring equipment. Copies of calibration certificates are provided in **Appendix B**.

**Table 3.2 Noise Monitoring Equipment**

Equipment	Model and Make	Qty.
Integrating Sound Level Meter	SVAN 955 & 957	4
Calibrator	B&K 4231 and SVAN 30A	3

#### Monitoring Parameters, Frequency and Duration

- 3.4 Table 3.3 summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix D**.

**Table 3.3 Noise Monitoring Parameters, Frequency and Duration**

Monitoring Stations	Parameter	Period	Frequency	Measurement
M1 M2 M3 M4(A)	L <sub>10</sub> (30 min.) dB(A) L <sub>90</sub> (30 min.) dB(A) L <sub>eq</sub> (30 min.) dB(A)	0700-1900 hrs on normal weekdays	Once per week	Façade

**Monitoring Methodology and QA/QC Procedures**

- The Sound Level Meter was set on a tripod at a height of 1.2 m above the ground.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting : A
  - time weighting : Fast
  - time measurement : 30 minutes
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the L<sub>eq</sub>, L<sub>90</sub> and L<sub>10</sub> were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Noise measurement was paused temporarily during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

**Maintenance and Calibration**

- 3.5 The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- 3.6 The sound level meter and calibrator were checked and calibrated at yearly intervals.
- 3.7 Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

## Results and Observations

- 3.8 Noise monitoring at the four designated locations was conducted as scheduled in the reporting month.
- 3.9 The summary of exceedance record in reporting month is shown in **Appendix H**. No exceedance was recorded for the noise monitoring.
- 3.10 The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented in Table 3.4.
- 3.11 Noise monitoring results and graphical presentations are shown in **Appendix G**.
- 3.12 The major noise source identified at the designated noise monitoring stations are as follows:

Monitoring Stations	Locations	Major Noise Source
M1	Buddhist Chi King Primary School	Traffic Noise Site vehicle movement
M2	S.K.H. Kowloon Bay Kei Lok Primary School	Excavation works
M3(A)	Kai Tak Operational Base	Traffic Noise Site vehicle movement Excavation works
M4	Lee Kau Yan Memorial School	Traffic Noise Site vehicle movement Excavation works

**Table 3.4 Baseline Noise Level and Noise Limit Level for Monitoring Stations**

Station	Baseline Noise Level, dB (A)	Noise Limit Level, dB (A)
M1	64.4 (at 0700 – 1900 hrs on normal weekdays)	70* (at 0700 – 1900 hrs on normal weekdays)
M2	61.3 (at 0700 – 1900 hrs on normal weekdays)	
M3(A)	65.8 (at 0700 – 1900 hrs on normal weekdays)	75 (at 0700 – 1900 hrs on normal weekdays)
M4	76.7 (at 0700 – 1900 hrs on normal weekdays)	70* (at 0700 – 1900 hrs on normal weekdays)

(\*) Noise Limit Level is 65 dB(A) during school examination periods.

**Table 3.5 Summary Table of Noise Monitoring Results during the Reporting Month**

Date	Measured Noise Level, Leq(30min) dB (A)	Baseline Level dB (A)	Construction Noise Level <sup>(1)</sup> : Leq(30min) dB (A)
M1 - Buddhist Chi King Primary School			
2-Nov-11	65.8	64.4	60.2
8-Nov-11	66.4		62.1
14-Nov-11	64.2		64.2
24-Nov-11	66.7		62.8
M2 - S.K.H. Kowloon Bay Kei Lok Primary School			
2-Nov-11	65.8	61.3	63.9
8-Nov-11	65.5		63.4
14-Nov-11	65.8		63.9
24-Nov-11	67.3		66.0
M3(A) – Kai Tak Operational Base			
1-Nov-11	65.2	65.8	65.2 Measured $\leq$ Baseline
7-Nov-11	65.9		49.5
17-Nov-11	66.5		58.2
23-Nov-11	67.4		62.3
29-Nov-11	64.7		64.7 Measured $\leq$ Baseline
M4 – Lee Kau Yan Memorial College			
1-Nov-11	75.6	76.7	75.6 Measured $\leq$ Baseline
7-Nov-11	73.5		73.5 Measured $\leq$ Baseline
17-Nov-11	73.1		73.1 Measured $\leq$ Baseline
23-Nov-11	72.5		72.5 Measured $\leq$ Baseline
29-Nov-11	76.5		76.5 Measured $\leq$ Baseline

(1) The noise level due to the construction work (CNL) was calculated by the following formula:

$$CNL = 10 \log (10^{MNL/10} - 10^{BNL/10})$$

Remarks: MNL = Measured Noise Level BNL = Baseline Noise Level

#### 4. COMPARISON OF EM&A RESULTS WITH EIA PREDICTIONS

4.1 The EM&A data was compared with the EIA predictions as summarized in 4.1 to 4.3.

**Table 4.1 Comparison of 1-hr TSP data with EIA predictions**

Station	Predicted 1-hr TSP conc.		
	Scenario1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	Reporting Month (Nov 11), $\mu\text{g}/\text{m}^3$
AM1(A) – Kai Tak Operational Base (Alternative station for Rhythm Garden)	192	298	126.6
AM2 – Lee Kau Yan Memorial School	290	312	133.5

**Table 4.2 Comparison of 24-hr TSP data with EIA predictions**

Station	Predicted 24-hr TSP conc.		
	Scenario1 (Mid 2009 to Mid 2013), $\mu\text{g}/\text{m}^3$	Scenario2 (Mid 2013 to Late 2016), $\mu\text{g}/\text{m}^3$	Reporting Month (Nov 11), $\mu\text{g}/\text{m}^3$
AM1(A) – Kai Tak Operational Base (Alternative station for Rhythm Garden)	121	156	63.1
AM2 – Lee Kau Yan Memorial School	145	169	78.5

**Table 4.3 Comparison of Noise Monitoring Data with EIA predictions**

Stations	Predicted Mitigated Construction Noise Levels during Normal Working Hour ( $L_{eq(30min)}$ dB(A))	Reporting Month (Nov 11), $L_{eq(30min)}$ dB(A)
M1 - Buddhist Chi King Primary School	51 – 68	60.2 – 64.2
M2 - S.K.H. Kowloon Bay Kei Lok Primary School	51 – 70	63.4 – 66.0
M3(A) - Kai Tak Operational Base (Alternative station for Cognitio College)	47 – 75	49.5 – 65.2
M4 - Lee Kau Yan Memorial School	47 – 74	72.5 – 76.5

- 4.2 The 1-hour and 24-hour average TSP concentration in the reporting month were well below the prediction in the approved Environmental Impact Assessment (EIA) Report and no Action/Limit Level exceedance was recorded.
- 4.3 The noise monitoring results in the reporting month was also within the range of predicted mitigated construction noise levels in the EIA report.
- 4.4 The discrepancy between the EM&A data and EIA predictions is considered due to road traffic noise from Prince Edward Road East which is the major noise source during the monitoring.

## 5. LANDSCAPE OF VISUAL

### Monitoring Requirements

- 5.1 According to EM&A Manual of the Kai Tak Development EIA Study, ET shall monitor and audit the contractor's operation during the construction period on a weekly basis, and to report on the contractor's compliance.

### Results and Observations

- 5.2 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of landscape and visual mitigation measures within the site boundaries of this Project. The summaries of site audits are attached in **Appendix I**.
- 5.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.
- 5.4 Should non-compliance of the landscape and visual impact occur, action in accordance with the action plan presented in **Appendix J** shall be performed.

## 6. ENVIRONMENTAL AUDIT

### Site Audits

- 6.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix I**.
- 6.2 Site audits were conducted on 3<sup>rd</sup>, 10<sup>th</sup>, 15<sup>th</sup> and 24<sup>th</sup> November 2011 in the reporting month. IEC site inspections were conducted on 15<sup>th</sup> November 2011. No non-compliance was observed during the site audits.

### Review of Environmental Monitoring Procedures

- 6.3 The monitoring works conducted by the monitoring team were inspected regularly. The following observations have been recorded for the monitoring works:

#### *Air Quality Monitoring*

- The monitoring team recorded all observations around the monitoring stations within and outside the construction site.
- The monitoring team recorded the temperature and weather conditions on the monitoring days.

#### *Noise Monitoring*

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- Major noise sources were identified and recorded. Other intrusive noise attributing to the result was trimmed off by pausing the monitoring temporarily.

### Status of Environmental Licensing and Permitting

- 6.4 All permits/licenses obtained for the Project are summarized in Table 6.1.

Permit No.	Valid Period		Details	Status
	From	To		
Environmental Permit (EP)				
EP-344/2009	23/4/09	N/A	Construction of a new sewage pumping station serving the planned Kai Tak development with installed capacity of more than 2,000 m <sup>3</sup> per day and a boundary of which is less than 150m from an existing or planned residential area or educational institution.	Valid
EP-337/2009	23/4/09	N/A	Construction of new distributor roads serving the planned Kai Tak development.	Valid
Effluent Discharge License				
WT-00011274-2011	-	31/12/16	Industrial discharge (near Kai Tak Tunnel)	Valid
WT-00011276/2011	-	31/12/16	Industrial discharge (near Concorde Road)	Valid



Permit No.	Valid Period		Details	Status
	From	To		
Registration of Chemical Waste Producer				
5213-286-P1079-04	-	N/A	Chemical Waste Types: Spent lubricating oil, spent solvent and spent battery containing heavy metals	Valid
Construction Noise Permit (CNP)				
NIL	N/A	N/A	N/A	N/A

### Status of Waste Management

- 6.5 The amount of wastes generated by the major site activities of this Project during the reporting month is shown in **Appendix M**.
- 6.6 In respect of the dump truck cover, the Contractor is advised to take record photos and inspection to ensure that all dump trucks have fully covered the skip before leaving the site.

### Implementation Status of Environmental Mitigation Measures

- 6.7 During site inspections in the reporting month, no non-conformance was identified. ET weekly site inspections were carried out during the reporting month and the observations and recommendations are summarized in Table 6.2.

**Table 6.2 Observations and Recommendations of Site Inspections**

Parameters	Date	Observations and Recommendations	Follow-up
<b>Water Quality</b>	10/11/2011	To clear the stagnant mud water after relevant construction of site PS1A is done.	Rectification/improvement was observed during the follow-up audit session.
	15/11/2011	The contractor is reminded to turn on the pump and remove stagnant water at box culvert BC6.	Rectification/improvement was observed during the follow-up audit session.
<b>Air Quality</b>	03/11/2011	To provide water spray for the exposed site area and during breaking works at stockpiling site.	Rectification/improvement was observed during the follow-up audit session.
	24/11/2011	To provide water spray for the exposed site area (Box Culvert BC6) more frequently.	Follow-up action is needed to be reviewed in the next reporting month.
<b>Noise</b>	15/11/2011	To provide valid noise label for the air compressor at the box culvert BC6.	Rectification/improvement was observed during the follow-up audit session.
<b>Waste/Chemical Management</b>	03/11/2011	To clear the chemical oil at the drip tray and oil spillage at PS1A properly.	Rectification/improvement was observed during the follow-up audit session.
	15/11/2011	To store the wooden boards in tidy manner.	Rectification/improvement was observed during the follow-up audit session.
	24/11/2011	To provide drip tray for the oil drums at Box Culvert BC6.	Follow-up action is needed to be reviewed in the next reporting month.

## Summary of Mitigation Measures Implemented

- 6.8 The monthly IEC audit was carried out on 15<sup>th</sup> November 2011 in reporting month, the observations were recorded and they are presented as follows:.

### 15<sup>th</sup> November 2011

#### Observations:

- Dusty stockpiles were observed near the box culvert site area. Tarpaulin sheet should be provided for stockpiles overnight to prevent dust emission.
- Haul roads/roads around site area were generally dry. The Contractor was reminded to spray water to minimize dust emission.
- Loading/transfer of dusty materials activity near the box culvert site area were observed. Water spraying should be provided when carrying loading/transferring dusty materials.
- Water ponding were observed at the box culvert site area/pumping room area. Proper drainage system should be maintained.

#### Follow up from last site walk:

- Open stockpiles of excavated materials were still observed at site BC6.

- 6.9 An updated summary of the EMIS is provided in **Appendix K**.

## Implementation Status of Event Action Plans

- 6.10 The Event Action Plans for air quality, noise and landscape and visual are presented in **Appendix J**.

### 1-hr TSP Monitoring

- 6.11 No Action/Limit Level exceedance was recorded in the reporting month.

### 24-hr TSP Monitoring

- 6.12 No Action/Limit Level exceedance was recorded in the reporting month.

### Construction Noise

- 6.13 No Action/Limit Level exceedance was recorded for construction noise.

### Landscape and visual

- 6.14 No non-compliance was recorded in the reporting month.

## Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

- 6.15 The summaries of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix L**.

## **7. FUTURE KEY ISSUES**

### **7.1 Major site activities undertaken for the coming two months include:**

- BC6 construction including excavation, steel fixing, formwork erection and concreting;
- Hoarding and fencing erection;
- Excavation with ELS at PS1A;
- Relocation of the surplus re-cycle grade 200 material;
- Backfilling to the abortive BC3 and BC5;
- Provision works for temporary drain along the existing Nullah No.2; and
- Provision works for cofferdam construction at the connection between BC6 and Kai Tak Nullah.

### **Key Issues for the Coming Month**

### **7.2 Key environmental issues in the coming month include:**

- Runoff from exposed slope;
- Wastewater and runoff discharge from site;
- Regular removal of silt, mud and sand along u-channels and sedimentation tanks;
- Review and implementation of temporary drainage system for the surface runoff;
- Noise from operation of the equipment, especially for rock-breaking activities, piling works and machinery on-site;
- Dust generation from stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- Watering for dust generating activity and on haul road;
- Proper storage of construction materials on site;
- Storage of chemicals/fuel and chemical waste/waste oil on site;
- Accumulation of general and construction waste on site.

### **7.3 The tentative program of major site activities and the impact prediction and control measures for the coming two months, i.e. January to February 2012 are summarized as follows:**

Construction Works	Major Impact Prediction	Control Measures
As mentioned in Section 7.1	Air quality impact (dust)	a) Frequent watering of haul road and unpaved/exposed areas; b) Frequent watering or covering stockpiles with tarpaulin or similar means; and c) Watering of any earth moving activities.
	Water quality impact (surface run-off)	d) Diversion of the collected effluent to de-silting facilities for treatment prior to discharge to public storm water drains; e) Provision of adequate de-silting facilities for treating surface run-off and other collected effluents prior to discharge; f) Provision of perimeter protection such as sealing of hoarding footings to avoid run-off from entering the existing storm water drainage system via public road; and g) Provision of measures to prevent discharge into the stream.
	Noise Impact	h) Scheduling of noisy construction activities if necessary to avoid persistent noisy operation; i) Controlling the number of plants use on site; j) Regular maintenance of machines; and k) Use of acoustic barriers if necessary.

#### Monitoring Schedule for the Next Month

7.4 The tentative environmental monitoring schedules for the next month are shown in **Appendix D**.

## **8. CONCLUSIONS AND RECOMMENDATIONS**

### **Conclusions**

- 8.1 Environmental monitoring works were performed in the reporting month and all monitoring results were checked and reviewed.

#### 1-hr TSP Monitoring

- 8.2 All 1-hr TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### 24-hr TSP Monitoring

- 8.3 All 24-hr TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Construction Noise Monitoring

- 8.4 All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Landscape and visual

- 8.5 No non-compliance was recorded in the reporting month.

#### Complaint and Prosecution

- 8.6 No environmental complaints and environmental prosecution were received in the reporting month.

### **Recommendations**

- 8.7 According to the environmental audit performed in the reporting month, the following recommendations were made:

#### *Air Quality Impact*

- To prohibit any open burning on site.
- To regularly maintain the quality of machinery and vehicles on site.
- To implement dust suppression measures on all haul roads, stockpiles, dry surfaces and excavation works.
- To provide hoarding along the entire length of that portion of the site boundary.

#### *Noise Impact*

- To inspect the noise sources inside the site.

- To space out noisy equipment and position the equipment as far away as possible from sensitive receivers.
- To provide temporary noise barriers for operations of noisy equipment near the noise sensitive receivers in an appropriate location.

#### *Water Impact*

- To prevent any surface runoff discharge into any stream course.
- To review and implement temporary drainage system.
- To identify any wastewater discharges from site.
- To ensure properly maintenance for de-silting facilities.
- To clear the silt and sediment in the sedimentation tanks.
- To review the capacity of de-silting facilities for discharge.
- To divert all the water generated from construction site to de-silting facilities with enough handling capacity before discharge.
- To avoid accumulation of stagnant and ponding water on site.

#### *Waste/Chemical Management*

- To check for any accumulation of waste materials or rubbish on site.
- To ensure the performance of sorting of C&D materials at source (during generation);
- To carry out inspection of dump truck at site exit to ensure inert and non-inert C&D materials are properly segregated before removing off site.
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the site.
- To avoid improper handling or storage of oil drum on site.

#### *Landscape and Visual*

- To protect the existing trees to be retained.
- To transplant the trees unavoidably affected by the works.
- To control of night-time lighting.
- To provide decorative screen hoarding.
- To complete landscape works at site area as early as possible.

---

---

## FIGURES

---

---



Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD	Scale	Project	CINOTECH
		N.T.S	No. MA11038	
Site Layout Plan		Date	Figure	
		Sep-11	1	

CINOTECH





Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD		Scale	N.T.S	Project No.	MA11038	CINOTECH
	Location of Air Quality Monitoring Stations		Date	Nov 11	Figure	2	




Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD		Scale	N.T.S	Project No.	MA11038	CINOTECH
	Location of Noise Monitoring Stations		Date	Nov-11	Figure	3	





Wind Data Monitoring Equipment set at Kai Tak Operational Base

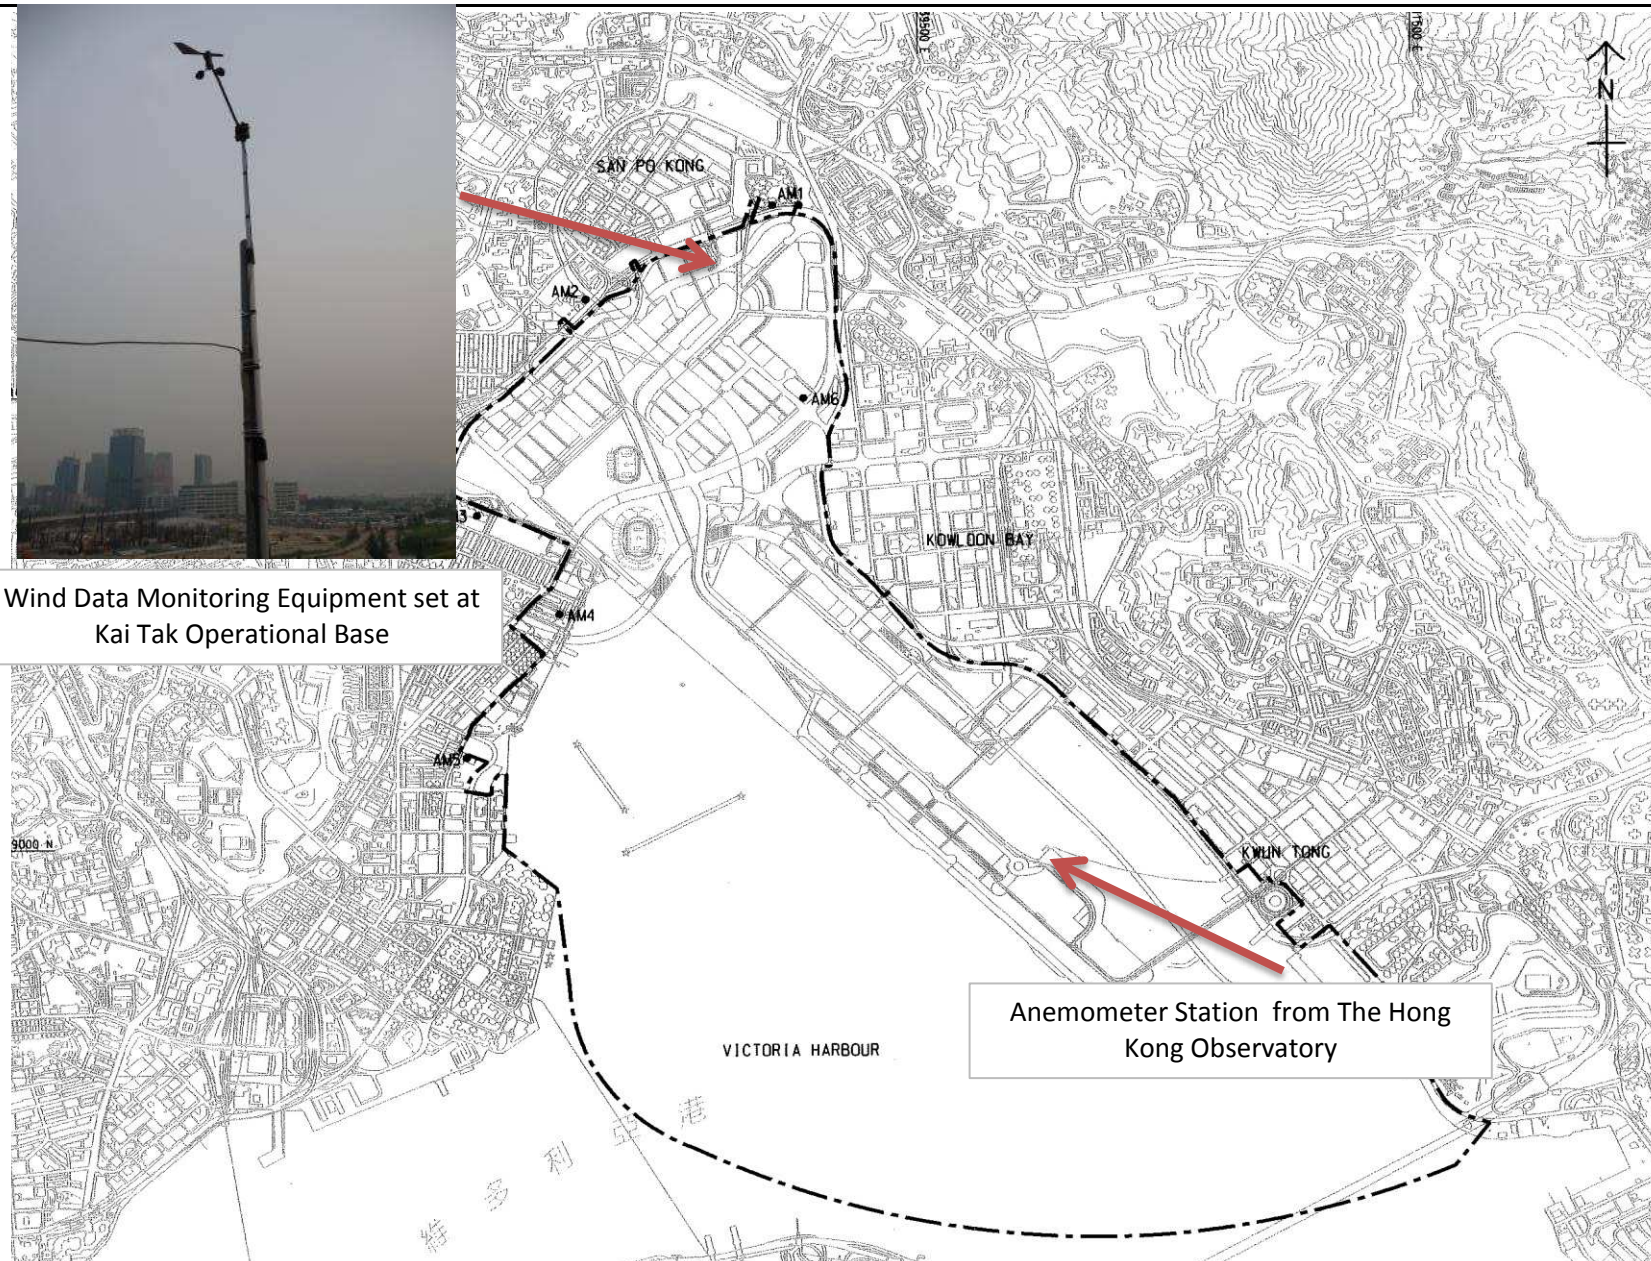

Anemometer Station from The Hong Kong Observatory

Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD	Scale	N.T.S	Project	No. MA11038	CINOTECH
	Location of Wind Data Monitoring Equipment	Date	Nov 11	Figure	4	



---

---

**APPENDIX A**  
**ACTION AND LIMIT LEVELS**

---

---

## Appendix A - Action and Limit Levels

**Table A-1 Action and Limit Levels for 1-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM1(A) – Kai Tak Operational Base	342	500
AM2 – Lee Kau Yan Memorial School	346	

**Table A-2 Action and Limit Levels for 24-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM1(A) – Kai Tak Operational Base	159	260
AM2 – Lee Kau Yan Memorial School	157	

**Table A-3 Action and Limit Levels for Construction Noise**

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) 70dB(A)/65dB(A)*

Remarks: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed. \*70dB(A) and 65dB(A) for schools during normal teaching periods and school examination periods, respectively.

---

---

**APPENDIX B  
COPIES OF CALIBRATION  
CERTIFICATES**

---

---

# High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA0040/58/0007

Station AM1(A) - Kai Tak Operational Base Operator: WK  
 Date: 3-Oct-11 Next Due Date: 2-Dec-11  
 Equipment No.: A-01-58 Serial No. 2357

Ambient Condition			
Temperature, Ta (K)	296.8	Pressure, Pa (mmHg)	758.2

Orifice Transfer Standard Information					
Equipment No.:	A-04-01	Slope, mc	0.0568	Intercept, bc	-0.0432
Last Calibration Date:	9-Oct-11	$mc \times Q_{std} + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	8-Oct-12	$Q_{std} = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	$Q_{std}$ (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.2	3.50	62.31	7.4	2.72
2	10.4	3.23	57.58	6.8	2.61
3	8.2	2.87	51.22	5.1	2.26
4	5.2	2.28	40.94	3.3	1.82
5	3.1	1.76	31.78	2.0	1.42

By Linear Regression of Y on X

Slope, mw = 0.0440 Intercept, bw = 0.0183

Correlation coefficient\* = 0.9980

\*If Correlation Coefficient < 0.990, check and recalibrate.

## Set Point Calculation

From the TSP Field Calibration Curve, take  $Q_{std} = 43$  CFM

From the Regression Equation, the "Y" value according to

$$mw \times Q_{std} + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point;  $W = (mw \times Q_{std} + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  3.65

Remarks:

Conducted by: Wk. Tang Signature: [Signature]  
 Checked by: Wk Signature: [Signature]

Date: 31/10/11  
 Date: 30 October 2011

# High-Volume TSP Sampler

## 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA0040/59/0007

Station AM2 - Lee Kau Yan Memorial School Operator: WK  
 Date: 3-Oct-11 Next Due Date: 2-Dec-11  
 Equipment No.: A-01-59 Serial No. 2354

Ambient Condition			
Temperature, Ta (K)	296.3	Pressure, Pa (mmHg)	758.4

Orifice Transfer Standard Information					
Equipment No.:	A-04-01	Slope, mc	0.0568	Intercept, bc	-0.0432
Last Calibration Date:	9-Oct-11	$mc \times Q_{std} + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	8-Oct-12	$Q_{std} = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.5	3.54	63.12	7.9	2.82
2	10.8	3.29	58.72	6.5	2.55
3	8.4	2.90	51.88	5.1	2.26
4	5.1	2.26	40.59	3.3	1.82
5	3.2	1.79	32.31	2.1	1.45

### By Linear Regression of Y on X

Slope, mw = 0.0431 Intercept, bw = 0.0564  
 Correlation coefficient\* = 0.9985

\*If Correlation Coefficient < 0.990, check and recalibrate.

### Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Q_{std} + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W =  $(mw \times Q_{std} + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  3.63

Remarks: \_\_\_\_\_

Conducted by: Wk Tang Signature: [Signature]  
 Checked by: [Signature] Signature: [Signature]

Date: 3/10/11  
 Date: 3 October 2011



## TEST REPORT

Description Calibration Orifice  
Serial No. 1536  
Model No. G25A  
Date 9 October 2011

Manufacturer Thermo Andersen  
Temperature, Ta (K) 298  
Pressure, Pa (mmHg) 762.3

Plate	Diff.Vol (m <sup>3</sup> )	Diff.Time (min)	Diff.Hg (mm)	Diff.H <sub>2</sub> O (in.)
1	1.00	1.3760	3.4	2.00
2	1.00	0.9740	6.4	4.00
3	1.00	0.8730	7.9	5.00
4	1.00	0.8320	8.6	5.50
5	1.00	0.6890	12.8	8.00

### DATA TABULATION

Vstd	(X axis) Qstd	(Y axis)
0.9985	0.7257	1.4163
0.9946	1.0211	2.0030
0.9926	1.1370	2.2394
0.9917	1.1919	2.3487
0.9861	1.4313	2.8326

Y axis=  $\text{SQRT}[\text{H}_2\text{O}(\text{Pa}/760)(298/\text{Ta})]$   
Qstd Slope ( m ) = 2.00766  
Intercept ( b ) = -0.04318  
Coefficient ( r ) = 0.99999

Va	(X axis) Qa	(Y axis)
0.9955	0.7235	0.8842
0.9916	1.0181	1.2505
0.9896	1.1336	1.3981
0.9887	1.1884	1.4664
0.9832	1.4270	1.7685

Y axis=  $\text{SQRT}[\text{H}_2\text{O}(\text{Ta}/\text{Pa})]$   
Qa Slope ( m ) = 1.25716  
Intercept ( b ) = -0.02696  
Coefficient ( r ) = 0.99999

### CALCULATIONS


$V_{\text{std}} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/760](298/\text{Ta})$   
 $Q_{\text{std}} = V_{\text{std}}/\text{Time}$   
 $V_{\text{a}} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/\text{Pa}]$   
 $Q_{\text{a}} = V_{\text{a}}/\text{Time}$

For subsequent flow rate calculations:  
 $Q_{\text{std}} = l/m\{[\text{SQRT}(\text{H}_2\text{O}(\text{Pa}/760)(298/\text{Ta}))] - b\}$   
 $Q_{\text{a}} = l/m\{[\text{SQRT}(\text{H}_2\text{O}(\text{Ta}/\text{Pa}))] - b\}$

PREPARED AND CHECKED BY:  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

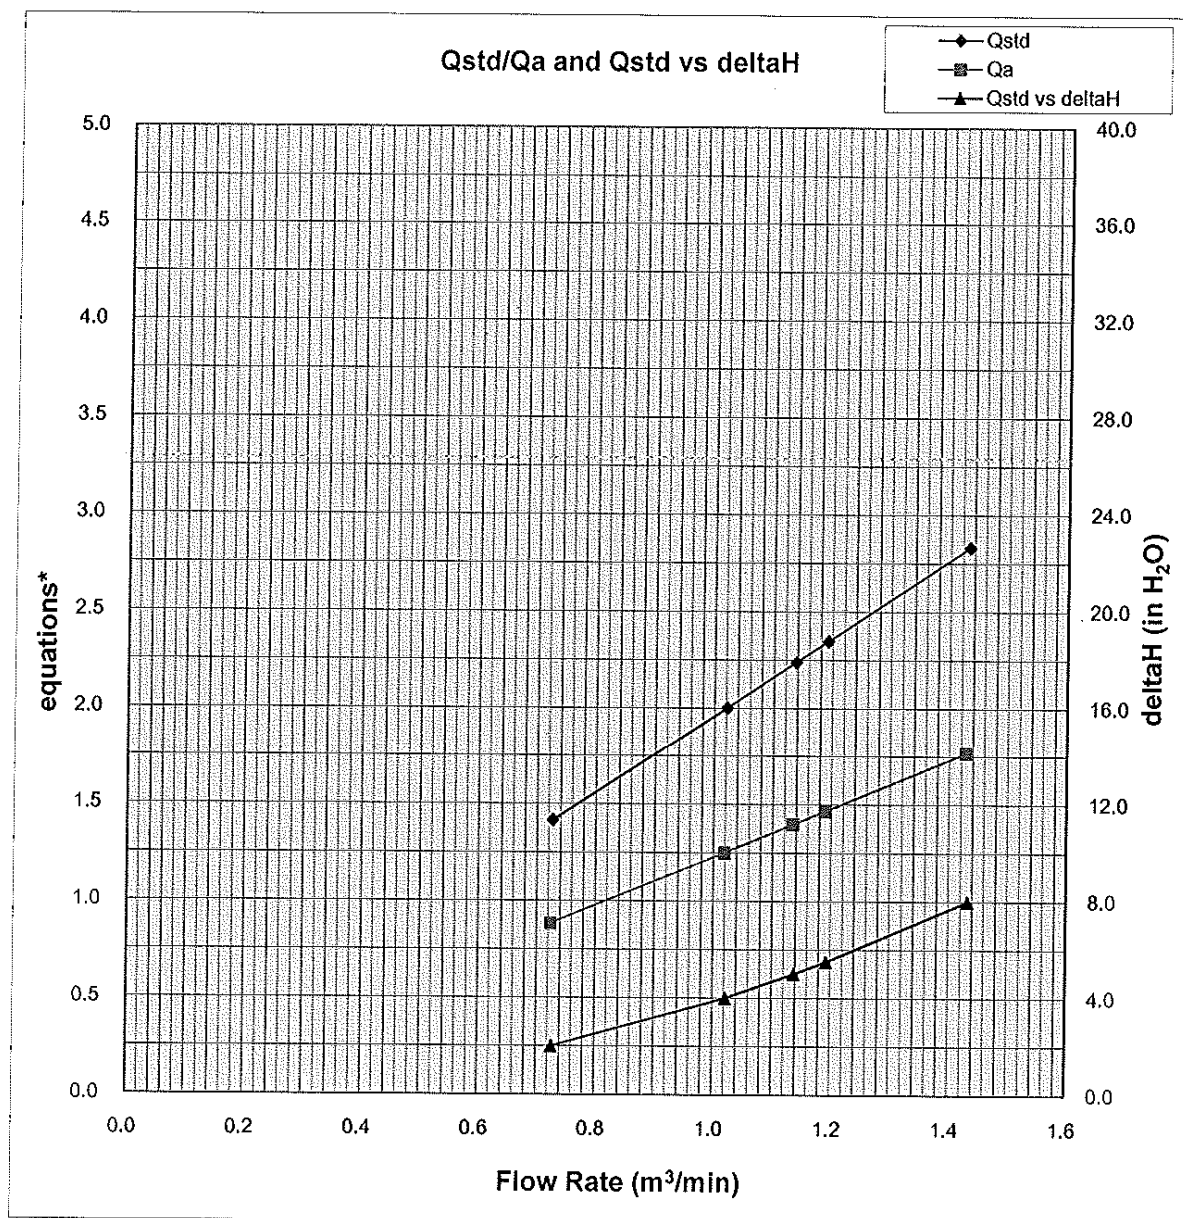

Y-axis equations:

Qstd series:  $\text{SQRT}[\Delta H(\text{Pa}/\text{Pstd})(\text{Tstd}/\text{Ta})]$

Qa series:  $\text{SQRT}[\Delta H(\text{Ta}/\text{Pa})]$

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/111021/1A
Date of Issue:	2011-10-24
Date Received:	2011-10-21
Date Tested:	2011-10-21
Date Completed:	2011-10-24
Next Due Date:	2011-12-23

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3
Serial No.	: 251634
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 550 CPM
Equipment No.	: A-02-01

**Test Conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 68%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0032
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/111007/1
Date of Issue:	2011-10-09
Date Received:	2011-10-07
Date Tested:	2011-10-07
Date Completed:	2011-10-09
Next Due Date:	2011-12-08

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3B
Serial No.	: 954253
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 685 CPM
Equipment No.	: A-02-05

**Test Conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 65%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0032
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/111021/1D
Date of Issue:	2011-10-24
Date Received:	2011-10-21
Date Tested:	2011-10-21
Date Completed:	2011-10-24
Next Due Date:	2011-12-23

**ATTN:** Mr. W. K. Tang

Page: 1 of 1

### Certificate of Calibration

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3B
Serial No.	: 095039
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 764 CPM
Equipment No.	: A-02-08

**Test Conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 68%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0031
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/111028/2
Date of Issue:	2011-10-31
Date Received:	2011-10-28
Date Tested:	2011-10-28
Date Completed:	2011-10-31
Next Due Date:	2011-12-30

**ATTN:** Mr. W. K. Tang

Page: 1 of 1

### Certificate of Calibration

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3B
Serial No.	: 095050
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 577 CPM
Equipment No.	: A-02-09

**Test Conditions:**

Room Temperature	: 22 degree Celsius
Relative Humidity	: 66%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0031
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/10/111106A
Date of Issue:	2011-11-07
Date Received:	2011-11-06
Date Tested:	2011-11-06
Date Completed:	2011-11-07
Next Due Date:	2012-05-06

**ATTN:** Miss Mei Ling Tang

Page: 1 of 2

### Certificate of Calibration

**Item for calibration:**

Description	: Weather Monitor II
Manufacturer	: Davis Instruments
Model No.	: 7440
Serial No.	: MC20813A11

**Test conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 48%

**Test Specifications:**

1. Performance check of anemometer
2. Performance check of wind direction sensor

**Methodology:**

In-house method with reference anemometer (RS232 Integral Vane Digital Anemometer)

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

Test Report No.:	C/10/111106A
Date of Issue:	2011-11-07
Date Received:	2011-11-06
Date Tested:	2011-11-06
Date Completed:	2011-11-07
Next Due Date:	2012-05-06

Page: 2 of 2

### Results:

#### 1. Performance check of anemometer

Air Velocity, m/s		Difference D (m/s)
Instrument Reading (V1)	Reference Value (V1)	D = V1 - V2
2.00	2.00	0.00

#### 2. Performance check of wind direction sensor

Wind Direction (°)		Difference D (°)
Instrument Reading (W1)	Reference Value (W2)	D = W1 - W2
0.0	0.0	0
45.1	45.0	0.1
90.2	90.5	-0.3
135.0	135.0	0
180.3	180.0	0.3
225.2	225.0	0.2
270.4	270.0	0.4
315.3	315.0	0.3
359.7	360.0	-0.3

\*\*\*\*\*END OF REPORT\*\*\*\*\*



## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/110117/1
Date of Issue:	2011-01-17
Date Received:	2011-01-14
Date Tested:	2011-01-14
Date Completed:	2011-01-17
Next Due Date:	2012-01-16

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 14302
Microphone No.	: 17204
Equipment No.	: N-08-04

**Test conditions:**

Room Temperature	: 22 degree Celsius
Relative Humidity	: 58%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/110124/1
Date of Issue:	2011-01-24
Date Received:	2011-01-21
Date Tested:	2011-01-21
Date Completed:	2011-01-24
Next Due Date:	2012-01-23

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 14303
Microphone No.	: 17204
Equipment No.	: N-08-05

**Test conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 55%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/100902/1
Date of Issue:	2011-09-03
Date Received:	2011-09-02
Date Tested:	2011-09-02
Date Completed:	2011-09-03
Next Due Date:	2012-09-02

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 21139
Microphone No.	: 43690
Equipment No.	: N-08-06

**Test conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 62%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/110906/3
Date of Issue:	2011-09-07
Date Received:	2011-09-06
Date Tested:	2011-09-06
Date Completed:	2011-09-07
Next Due Date:	2012-09-06

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 21460
Microphone No.	: 43679
Equipment No.	: N-08-09

**Test conditions:**

Room Temperature	: 22 degree Celsius
Relative Humidity	: 66%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/110902-3
Date of Issue:	2011-09-03
Date Received:	2011-09-02
Date Tested:	2011-09-02
Date Completed:	2011-09-03
Next Due Date:	2012-09-02

**ATTN:** Mr. Henry Leung

**Item for calibration:**

Description	: Acoustical Calibrator
Manufacturer	: Brüel & Kjær
Model No.	: 4231
Serial No.	: 2412367
Equipment No.	: N-02-03

**Test conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 62%

**Methodology:**

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/110923/2
Date of Issue:	2011-09-24
Date Received:	2011-09-23
Date Tested:	2011-09-23
Date Completed:	2011-09-24
Next Due Date:	2012-09-23

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10929
Equipment No.	: N-09-01

### Test conditions:

Room Temperatre	: 23 degree Celsius
Relative Humidity	: 59%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 $\pm$ 0.1 dB
At 114 dB SPL	114.0	114.0 $\pm$ 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/111104/1
Date of Issue:	2011-11-05
Date Received:	2011-11-04
Date Tested:	2011-11-04
Date Completed:	2011-11-05
Next Due Date:	2012-11-04

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10965
Equipment No.	: N-09-02

### Test conditions:

Room Temperature	: 23 degree Celsius
Relative Humidity	: 60%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

---

---

**APPENDIX C**  
**WEATHER INFORMATION**

---

---



**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**I. General Information**

<b>Date</b>	<b>Mean Air Temperature (°C)</b>	<b>Mean Relative Humidity (%)</b>	<b>Precipitation (mm)</b>
1 November 2011	22.3 – 27.7	52 – 83	0
2 November 2011	23.3 – 28.9	55 – 84	0
3 November 2011	24.1 – 29.0	63 – 86	0
4 November 2011	24.7 – 29.7	60 – 86	Trace
5 November 2011	24.8 – 28.8	72 – 89	Trace
6 November 2011	25.7 – 28.8	71 – 83	Trace
7 November 2011	24.3 – 28.0	69 – 85	Trace
8 November 2011	21.9 – 24.3	88 – 97	13.9
9 November 2011	18.8 – 21.1	82 – 98	44.2
10 November 2011	17.7 – 21.2	68 – 91	0.2
11 November 2011	18.1 – 22.0	65 – 79	Trace
12 November 2011	19.6 – 24.7	60 – 83	0
13 November 2011	21.1 – 26.6	58 – 87	0
14 November 2011	22.6 – 25.3	73 – 88	Trace
15 November 2011	22.1 – 26.2	67 – 81	0
16 November 2011	21.7 – 25.5	69 – 85	0
17 November 2011	22.6 – 24.5	75 – 99	18.1
18 November 2011	22.6 – 26.9	83 – 99	8.6
19 November 2011	23.7 – 26.4	71 – 98	1.1

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**I. General Information**

<b>Date</b>	<b>Mean Air Temperature (°C)</b>	<b>Mean Relative Humidity (%)</b>	<b>Precipitation (mm)</b>
20 November 2011	21.2 – 24.4	67 – 82	Trace
21 November 2011	20.8 – 22.3	59 – 76	Trace
22 November 2011	20.2 – 23.7	58 – 78	Trace
23 November 2011	20.7 – 23.8	54 – 70	Trace
24 November 2011	18.7 – 22.7	58 – 77	0
25 November 2011	19.6 – 21.3	61 – 80	0
26 November 2011	20.1 – 22.3	63 – 79	Trace
27 November 2011	19.3 – 24.5	61 – 87	0
28 November 2011	20.2 – 24.7	65 – 89	0
29 November 2011	21.6 – 25.0	65 – 85	0
30 November 2011	21.5 – 26.3	66 – 87	Trace

\* The above information was extracted from the daily weather summary by Hong Kong Observatory.

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

<b>Date</b>	<b>Time</b>	<b>Wind Speed m/s</b>	<b>Direction</b>
1-Nov-2011	0:00	1.7	E
1-Nov-2011	1:00	1.7	ENE
1-Nov-2011	2:00	1.8	ESE
1-Nov-2011	3:00	1.8	E
1-Nov-2011	4:00	1.5	SSE
1-Nov-2011	5:00	1.4	WSW
1-Nov-2011	6:00	1.5	SW
1-Nov-2011	7:00	1.4	WSW
1-Nov-2011	8:00	1.6	ENE
1-Nov-2011	9:00	1.6	SSW
1-Nov-2011	10:00	1.7	SSW
1-Nov-2011	11:00	2.1	NE
1-Nov-2011	12:00	2.2	NE
1-Nov-2011	13:00	1.8	E
1-Nov-2011	14:00	1.9	ENE
1-Nov-2011	15:00	1.8	N
1-Nov-2011	16:00	1.8	NE
1-Nov-2011	17:00	1.5	SW
1-Nov-2011	18:00	1.4	SE
1-Nov-2011	19:00	1.4	S
1-Nov-2011	20:00	1.1	SW
1-Nov-2011	21:00	1.3	SW
1-Nov-2011	22:00	1.3	SE
1-Nov-2011	23:00	1.3	SSE
2-Nov-2011	0:00	1.3	SSE
2-Nov-2011	1:00	1.3	NNE
2-Nov-2011	2:00	1.6	ENE
2-Nov-2011	3:00	1.5	ENE
2-Nov-2011	4:00	1.3	ESE
2-Nov-2011	5:00	1.4	SE
2-Nov-2011	6:00	1.6	N
2-Nov-2011	7:00	1.6	E
2-Nov-2011	8:00	1.5	NNE
2-Nov-2011	9:00	1.6	ESE
2-Nov-2011	10:00	1.8	ESE
2-Nov-2011	11:00	1.8	ESE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

2-Nov-2011	12:00	2.2	SSE
2-Nov-2011	13:00	2.3	SSE
2-Nov-2011	14:00	2.3	SW
2-Nov-2011	15:00	2.2	SSW
2-Nov-2011	16:00	2.0	SSW
2-Nov-2011	17:00	2.0	SW
2-Nov-2011	18:00	1.7	WSW
2-Nov-2011	19:00	1.4	WSW
2-Nov-2011	20:00	1.4	E
2-Nov-2011	21:00	1.7	ENE
2-Nov-2011	22:00	1.8	WSW
2-Nov-2011	23:00	2.0	SW
3-Nov-2011	0:00	1.8	SW
3-Nov-2011	1:00	1.8	N
3-Nov-2011	2:00	1.7	WSW
3-Nov-2011	3:00	1.9	S
3-Nov-2011	4:00	2.1	ESE
3-Nov-2011	5:00	1.8	ESE
3-Nov-2011	6:00	1.8	ESE
3-Nov-2011	7:00	1.7	ENE
3-Nov-2011	8:00	1.9	W
3-Nov-2011	9:00	1.4	SW
3-Nov-2011	10:00	1.9	SW
3-Nov-2011	11:00	2.0	WSW
3-Nov-2011	12:00	1.8	N
3-Nov-2011	13:00	1.8	SW
3-Nov-2011	14:00	1.8	WSW
3-Nov-2011	15:00	1.6	SSW
3-Nov-2011	16:00	1.5	NE
3-Nov-2011	17:00	1.5	NW
3-Nov-2011	18:00	1.2	ENE
3-Nov-2011	19:00	1.2	W
3-Nov-2011	20:00	1.4	WSW
3-Nov-2011	21:00	1.0	W
3-Nov-2011	22:00	1.2	W
3-Nov-2011	23:00	1.4	W
4-Nov-2011	0:00	1.8	W

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

4-Nov-2011	1:00	1.4	SW
4-Nov-2011	2:00	1.6	SW
4-Nov-2011	3:00	1.5	SW
4-Nov-2011	4:00	1.7	SW
4-Nov-2011	5:00	1.8	SW
4-Nov-2011	6:00	2.1	N
4-Nov-2011	7:00	1.9	NE
4-Nov-2011	8:00	2.0	SSE
4-Nov-2011	9:00	2.2	SE
4-Nov-2011	10:00	2.6	ENE
4-Nov-2011	11:00	2.4	SSE
4-Nov-2011	12:00	2.4	ENE
4-Nov-2011	13:00	2.3	SSW
4-Nov-2011	14:00	2.0	ENE
4-Nov-2011	15:00	2.4	ENE
4-Nov-2011	16:00	2.1	ENE
4-Nov-2011	17:00	1.9	SE
4-Nov-2011	18:00	1.8	SE
4-Nov-2011	19:00	1.4	SSE
4-Nov-2011	20:00	1.2	SE
4-Nov-2011	21:00	1.4	SE
4-Nov-2011	22:00	1.5	SW
4-Nov-2011	23:00	1.3	SW
5-Nov-2011	0:00	1.2	WNW
5-Nov-2011	1:00	1.4	SW
5-Nov-2011	2:00	1.4	S
5-Nov-2011	3:00	1.4	SSE
5-Nov-2011	4:00	1.4	ENE
5-Nov-2011	5:00	1.5	SE
5-Nov-2011	6:00	1.2	SE
5-Nov-2011	7:00	1.2	S
5-Nov-2011	8:00	1.4	S
5-Nov-2011	9:00	1.8	SE
5-Nov-2011	10:00	2.2	ESE
5-Nov-2011	11:00	2.2	ESE
5-Nov-2011	12:00	2.4	SW
5-Nov-2011	13:00	2.5	ENE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

5-Nov-2011	14:00	2.6	ENE
5-Nov-2011	15:00	2.5	ENE
5-Nov-2011	16:00	2.4	ENE
5-Nov-2011	17:00	2.4	ENE
5-Nov-2011	18:00	2.4	ESE
5-Nov-2011	19:00	2.2	NE
5-Nov-2011	20:00	2.0	N
5-Nov-2011	21:00	1.8	N
5-Nov-2011	22:00	1.8	N
5-Nov-2011	23:00	1.7	WSW
6-Nov-2011	0:00	1.6	NNE
6-Nov-2011	1:00	1.7	WNW
6-Nov-2011	2:00	1.8	ESE
6-Nov-2011	3:00	1.9	SE
6-Nov-2011	4:00	1.8	SE
6-Nov-2011	5:00	2.3	SE
6-Nov-2011	6:00	2.2	ENE
6-Nov-2011	7:00	2.3	SSW
6-Nov-2011	8:00	2.2	E
6-Nov-2011	9:00	2.4	N
6-Nov-2011	10:00	2.9	ENE
6-Nov-2011	11:00	3.0	ENE
6-Nov-2011	12:00	2.8	NE
6-Nov-2011	13:00	2.9	E
6-Nov-2011	14:00	3.1	SE
6-Nov-2011	15:00	3.0	SSE
6-Nov-2011	16:00	2.6	SE
6-Nov-2011	17:00	2.3	ENE
6-Nov-2011	18:00	2.2	ENE
6-Nov-2011	19:00	2.0	ENE
6-Nov-2011	20:00	1.9	ENE
6-Nov-2011	21:00	1.8	NE
6-Nov-2011	22:00	1.5	NE
6-Nov-2011	23:00	1.7	NNE
7-Nov-2011	0:00	1.7	NNE
7-Nov-2011	1:00	1.8	NNE
7-Nov-2011	2:00	1.8	NE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

7-Nov-2011	3:00	1.9	ESE
7-Nov-2011	4:00	1.8	E
7-Nov-2011	5:00	1.9	SSE
7-Nov-2011	6:00	1.9	NNE
7-Nov-2011	7:00	1.8	NE
7-Nov-2011	8:00	2.1	NE
7-Nov-2011	9:00	2.6	NE
7-Nov-2011	10:00	2.2	ENE
7-Nov-2011	11:00	2.3	ENE
7-Nov-2011	12:00	2.2	NE
7-Nov-2011	13:00	2.0	NE
7-Nov-2011	14:00	2.0	ENE
7-Nov-2011	15:00	2.2	E
7-Nov-2011	16:00	1.9	SE
7-Nov-2011	17:00	1.9	SE
7-Nov-2011	18:00	1.8	SE
7-Nov-2011	19:00	1.7	SE
7-Nov-2011	20:00	1.5	SE
7-Nov-2011	21:00	1.4	ESE
7-Nov-2011	22:00	1.4	ENE
7-Nov-2011	23:00	1.4	ENE
8-Nov-2011	0:00	1.4	ENE
8-Nov-2011	1:00	1.5	ESE
8-Nov-2011	2:00	1.3	ESE
8-Nov-2011	3:00	1.3	ESE
8-Nov-2011	4:00	1.9	SSE
8-Nov-2011	5:00	2.0	ENE
8-Nov-2011	6:00	1.9	NE
8-Nov-2011	7:00	1.9	NE
8-Nov-2011	8:00	2.0	NE
8-Nov-2011	9:00	1.9	NE
8-Nov-2011	10:00	1.9	NE
8-Nov-2011	11:00	1.9	ENE
8-Nov-2011	12:00	2.3	ENE
8-Nov-2011	13:00	2.1	ENE
8-Nov-2011	14:00	2.2	ENE
8-Nov-2011	15:00	2.1	ENE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

8-Nov-2011	16:00	2.2	ENE
8-Nov-2011	17:00	1.8	NE
8-Nov-2011	18:00	1.6	NNE
8-Nov-2011	19:00	1.4	NNE
8-Nov-2011	20:00	1.3	NNE
8-Nov-2011	21:00	1.4	NNE
8-Nov-2011	22:00	1.3	NNE
8-Nov-2011	23:00	1.1	NNE
9-Nov-2011	0:00	1.4	NE
9-Nov-2011	1:00	1.4	NE
9-Nov-2011	2:00	1.4	ENE
9-Nov-2011	3:00	1.4	NNE
9-Nov-2011	4:00	1.6	NNE
9-Nov-2011	5:00	1.6	NNE
9-Nov-2011	6:00	1.4	NNE
9-Nov-2011	7:00	1.3	NE
9-Nov-2011	8:00	1.5	ENE
9-Nov-2011	9:00	1.8	ENE
9-Nov-2011	10:00	1.6	NE
9-Nov-2011	11:00	1.8	NE
9-Nov-2011	12:00	1.7	ENE
9-Nov-2011	13:00	1.8	NE
9-Nov-2011	14:00	1.7	NE
9-Nov-2011	15:00	1.7	NE
9-Nov-2011	16:00	1.6	NE
9-Nov-2011	17:00	1.4	ENE
9-Nov-2011	18:00	1.2	NNE
9-Nov-2011	19:00	1.0	NNE
9-Nov-2011	20:00	0.9	NE
9-Nov-2011	21:00	1.2	N
9-Nov-2011	22:00	1.1	NE
9-Nov-2011	23:00	1.1	NNE
10-Nov-2011	0:00	0.9	NNE
10-Nov-2011	1:00	1.0	NNE
10-Nov-2011	2:00	1.1	NE
10-Nov-2011	3:00	1.1	NE
10-Nov-2011	4:00	1.1	NNE



**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

10-Nov-2011	5:00	1.0	NNE
10-Nov-2011	6:00	1.1	NNE
10-Nov-2011	7:00	1.1	NNE
10-Nov-2011	8:00	1.3	NNE
10-Nov-2011	9:00	1.4	NNE
10-Nov-2011	10:00	1.7	NNE
10-Nov-2011	11:00	1.8	NE
10-Nov-2011	12:00	1.8	NE
10-Nov-2011	13:00	2.0	ENE
10-Nov-2011	14:00	2.1	SSE
10-Nov-2011	15:00	1.9	E
10-Nov-2011	16:00	1.6	SE
10-Nov-2011	17:00	1.6	NNE
10-Nov-2011	18:00	1.5	N
10-Nov-2011	19:00	1.0	NNE
10-Nov-2011	20:00	1.0	NE
10-Nov-2011	21:00	1.2	NE
10-Nov-2011	22:00	1.3	ENE
10-Nov-2011	23:00	0.9	NE
11-Nov-2011	0:00	1.1	NE
11-Nov-2011	1:00	1.4	NE
11-Nov-2011	2:00	1.6	NNE
11-Nov-2011	3:00	1.2	ENE
11-Nov-2011	4:00	1.2	ENE
11-Nov-2011	5:00	1.3	ENE
11-Nov-2011	6:00	1.2	NNE
11-Nov-2011	7:00	1.2	N
11-Nov-2011	8:00	1.5	NE
11-Nov-2011	9:00	1.5	SE
11-Nov-2011	10:00	1.6	SE
11-Nov-2011	11:00	2.0	SE
11-Nov-2011	12:00	2.0	WSW
11-Nov-2011	13:00	1.8	WSW
11-Nov-2011	14:00	1.7	SW
11-Nov-2011	15:00	1.6	ESE
11-Nov-2011	16:00	1.6	SSW
11-Nov-2011	17:00	1.6	SW

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

11-Nov-2011	18:00	1.8	ENE
11-Nov-2011	19:00	1.8	S
11-Nov-2011	20:00	1.7	S
11-Nov-2011	21:00	1.5	ENE
11-Nov-2011	22:00	1.6	NE
11-Nov-2011	23:00	1.9	NE
12-Nov-2011	0:00	2.0	NE
12-Nov-2011	1:00	1.8	ENE
12-Nov-2011	2:00	1.8	ENE
12-Nov-2011	3:00	1.6	NE
12-Nov-2011	4:00	1.6	ENE
12-Nov-2011	5:00	1.9	NE
12-Nov-2011	6:00	1.7	ENE
12-Nov-2011	7:00	2.0	N
12-Nov-2011	8:00	2.2	N
12-Nov-2011	9:00	2.2	N
12-Nov-2011	10:00	2.2	W
12-Nov-2011	11:00	2.5	SSW
12-Nov-2011	12:00	2.3	SW
12-Nov-2011	13:00	2.2	SW
12-Nov-2011	14:00	2.2	SW
12-Nov-2011	15:00	2.1	SW
12-Nov-2011	16:00	2.3	SW
12-Nov-2011	17:00	2.1	SW
12-Nov-2011	18:00	1.9	SW
12-Nov-2011	19:00	1.6	SW
12-Nov-2011	20:00	1.5	ENE
12-Nov-2011	21:00	1.4	ENE
12-Nov-2011	22:00	1.3	ENE
12-Nov-2011	23:00	1.7	ENE
13-Nov-2011	0:00	1.8	ENE
13-Nov-2011	1:00	2.0	SW
13-Nov-2011	2:00	1.7	SW
13-Nov-2011	3:00	1.8	WNW
13-Nov-2011	4:00	1.7	WNW
13-Nov-2011	5:00	1.9	WNW
13-Nov-2011	6:00	1.9	WNW

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

13-Nov-2011	7:00	2.2	ENE
13-Nov-2011	8:00	2.2	ENE
13-Nov-2011	9:00	2.0	WSW
13-Nov-2011	10:00	2.1	WSW
13-Nov-2011	11:00	2.4	WSW
13-Nov-2011	12:00	2.4	NNE
13-Nov-2011	13:00	2.4	NNE
13-Nov-2011	14:00	2.6	NE
13-Nov-2011	15:00	2.5	NNE
13-Nov-2011	16:00	2.2	NNE
13-Nov-2011	17:00	2.1	NE
13-Nov-2011	18:00	2.1	NNE
13-Nov-2011	19:00	1.9	NNE
13-Nov-2011	20:00	1.3	NNE
13-Nov-2011	21:00	1.4	NNE
13-Nov-2011	22:00	1.8	NE
13-Nov-2011	23:00	1.5	ENE
14-Nov-2011	0:00	1.9	NE
14-Nov-2011	1:00	2.0	ENE
14-Nov-2011	2:00	1.9	ENE
14-Nov-2011	3:00	1.8	ENE
14-Nov-2011	4:00	1.8	ENE
14-Nov-2011	5:00	1.8	ENE
14-Nov-2011	6:00	1.9	E
14-Nov-2011	7:00	1.9	E
14-Nov-2011	8:00	1.9	E
14-Nov-2011	9:00	2.1	NNE
14-Nov-2011	10:00	2.3	ENE
14-Nov-2011	11:00	2.7	NNE
14-Nov-2011	12:00	3.1	NE
14-Nov-2011	13:00	2.8	N
14-Nov-2011	14:00	2.6	N
14-Nov-2011	15:00	2.9	NNE
14-Nov-2011	16:00	2.8	NW
14-Nov-2011	17:00	2.8	N
14-Nov-2011	18:00	2.5	N
14-Nov-2011	19:00	2.4	ENE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

14-Nov-2011	20:00	2.4	ENE
14-Nov-2011	21:00	2.6	NNE
14-Nov-2011	22:00	2.6	NE
14-Nov-2011	23:00	2.6	SSE
15-Nov-2011	0:00	2.5	SSE
15-Nov-2011	1:00	2.8	ENE
15-Nov-2011	2:00	2.4	ENE
15-Nov-2011	3:00	2.4	ENE
15-Nov-2011	4:00	2.5	ENE
15-Nov-2011	5:00	2.8	NNE
15-Nov-2011	6:00	2.9	ENE
15-Nov-2011	7:00	2.5	ENE
15-Nov-2011	8:00	2.4	ESE
15-Nov-2011	9:00	2.4	SE
15-Nov-2011	10:00	2.4	SE
15-Nov-2011	11:00	2.6	SE
15-Nov-2011	12:00	2.4	NNE
15-Nov-2011	13:00	2.2	NE
15-Nov-2011	14:00	2.5	ENE
15-Nov-2011	15:00	2.6	ENE
15-Nov-2011	16:00	2.3	NE
15-Nov-2011	17:00	2.7	NNE
15-Nov-2011	18:00	2.8	NE
15-Nov-2011	19:00	2.5	NNE
15-Nov-2011	20:00	2.4	ENE
15-Nov-2011	21:00	2.6	E
15-Nov-2011	22:00	2.5	ENE
15-Nov-2011	23:00	2.7	NE
16-Nov-2011	0:00	2.3	NE
16-Nov-2011	1:00	2.5	SSE
16-Nov-2011	2:00	2.3	NE
16-Nov-2011	3:00	2.0	NE
16-Nov-2011	4:00	2.2	SSE
16-Nov-2011	5:00	2.3	ENE
16-Nov-2011	6:00	1.9	NE
16-Nov-2011	7:00	2.0	NNE
16-Nov-2011	8:00	1.9	NE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

16-Nov-2011	9:00	1.8	NNE
16-Nov-2011	10:00	2.1	NNE
16-Nov-2011	11:00	2.2	NE
16-Nov-2011	12:00	2.4	NNE
16-Nov-2011	13:00	2.7	NNE
16-Nov-2011	14:00	2.5	NE
16-Nov-2011	15:00	2.4	SE
16-Nov-2011	16:00	2.3	SSW
16-Nov-2011	17:00	2.5	W
16-Nov-2011	18:00	1.8	WNW
16-Nov-2011	19:00	1.6	W
16-Nov-2011	20:00	1.3	WSW
16-Nov-2011	21:00	1.6	W
16-Nov-2011	22:00	1.3	W
16-Nov-2011	23:00	1.3	W
17-Nov-2011	0:00	1.4	WNW
17-Nov-2011	1:00	1.4	W
17-Nov-2011	2:00	1.3	WSW
17-Nov-2011	3:00	1.4	WSW
17-Nov-2011	4:00	1.3	SW
17-Nov-2011	5:00	1.2	W
17-Nov-2011	6:00	1.7	WNW
17-Nov-2011	7:00	1.9	WNW
17-Nov-2011	8:00	2.0	WNW
17-Nov-2011	9:00	2.0	W
17-Nov-2011	10:00	2.3	W
17-Nov-2011	11:00	2.3	WNW
17-Nov-2011	12:00	2.4	W
17-Nov-2011	13:00	2.7	W
17-Nov-2011	14:00	2.4	W
17-Nov-2011	15:00	2.3	WSW
17-Nov-2011	16:00	2.1	WSW
17-Nov-2011	17:00	1.8	SSE
17-Nov-2011	18:00	1.9	S
17-Nov-2011	19:00	1.5	S
17-Nov-2011	20:00	1.6	S
17-Nov-2011	21:00	1.6	W

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

17-Nov-2011	22:00	1.8	W
17-Nov-2011	23:00	1.9	SSW
18-Nov-2011	0:00	1.9	SW
18-Nov-2011	1:00	1.5	SSE
18-Nov-2011	2:00	1.8	SW
18-Nov-2011	3:00	1.6	SW
18-Nov-2011	4:00	1.6	WSW
18-Nov-2011	5:00	1.7	WSW
18-Nov-2011	6:00	1.7	SSW
18-Nov-2011	7:00	1.4	SSW
18-Nov-2011	8:00	1.4	SSW
18-Nov-2011	9:00	1.6	S
18-Nov-2011	10:00	2.2	S
18-Nov-2011	11:00	2.1	SSW
18-Nov-2011	12:00	2.0	WSW
18-Nov-2011	13:00	2.2	W
18-Nov-2011	14:00	2.3	S
18-Nov-2011	15:00	2.1	SW
18-Nov-2011	16:00	2.0	NNW
18-Nov-2011	17:00	1.8	SW
18-Nov-2011	18:00	1.7	W
18-Nov-2011	19:00	1.7	W
18-Nov-2011	20:00	1.7	WNW
18-Nov-2011	21:00	2.0	NW
18-Nov-2011	22:00	2.0	N
18-Nov-2011	23:00	1.7	WNW
19-Nov-2011	0:00	1.8	NE
19-Nov-2011	1:00	1.6	S
19-Nov-2011	2:00	1.7	E
19-Nov-2011	3:00	1.7	W
19-Nov-2011	4:00	1.9	NE
19-Nov-2011	5:00	1.9	NNE
19-Nov-2011	6:00	2.0	NE
19-Nov-2011	7:00	1.9	ENE
19-Nov-2011	8:00	2.2	NE
19-Nov-2011	9:00	2.1	ENE
19-Nov-2011	10:00	2.3	WNW

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

19-Nov-2011	11:00	2.5	NE
19-Nov-2011	12:00	2.7	NNE
19-Nov-2011	13:00	2.8	NNE
19-Nov-2011	14:00	2.5	NE
19-Nov-2011	15:00	2.6	NNE
19-Nov-2011	16:00	2.4	ENE
19-Nov-2011	17:00	2.4	NE
19-Nov-2011	18:00	1.4	ENE
19-Nov-2011	19:00	1.4	NE
19-Nov-2011	20:00	1.2	NE
19-Nov-2011	21:00	1.2	ENE
19-Nov-2011	22:00	1.2	SE
19-Nov-2011	23:00	1.3	WNW
20-Nov-2011	0:00	1.3	WNW
20-Nov-2011	1:00	1.3	WNW
20-Nov-2011	2:00	1.4	W
20-Nov-2011	3:00	1.6	SW
20-Nov-2011	4:00	1.2	SW
20-Nov-2011	5:00	1.5	W
20-Nov-2011	6:00	1.6	W
20-Nov-2011	7:00	1.3	WNW
20-Nov-2011	8:00	1.6	W
20-Nov-2011	9:00	2.0	W
20-Nov-2011	10:00	2.4	S
20-Nov-2011	11:00	2.3	SSE
20-Nov-2011	12:00	2.5	SW
20-Nov-2011	13:00	2.5	WSW
20-Nov-2011	14:00	2.5	W
20-Nov-2011	15:00	2.6	WSW
20-Nov-2011	16:00	2.1	SW
20-Nov-2011	17:00	2.0	W
20-Nov-2011	18:00	1.8	W
20-Nov-2011	19:00	1.5	W
20-Nov-2011	20:00	1.4	W
20-Nov-2011	21:00	1.6	W
20-Nov-2011	22:00	1.7	W
20-Nov-2011	23:00	1.9	W

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

21-Nov-2011	0:00	1.7	SW
21-Nov-2011	1:00	1.6	SW
21-Nov-2011	2:00	1.8	SW
21-Nov-2011	3:00	1.9	SW
21-Nov-2011	4:00	2.0	WNW
21-Nov-2011	5:00	1.6	WNW
21-Nov-2011	6:00	1.7	W
21-Nov-2011	7:00	1.9	W
21-Nov-2011	8:00	1.8	WNW
21-Nov-2011	9:00	2.0	W
21-Nov-2011	10:00	2.2	SW
21-Nov-2011	11:00	2.5	WNW
21-Nov-2011	12:00	2.4	WNW
21-Nov-2011	13:00	2.6	WNW
21-Nov-2011	14:00	2.4	WNW
21-Nov-2011	15:00	2.6	W
21-Nov-2011	16:00	2.6	WNW
21-Nov-2011	17:00	2.6	WNW
21-Nov-2011	18:00	2.5	WNW
21-Nov-2011	19:00	2.7	W
21-Nov-2011	20:00	2.7	W
21-Nov-2011	21:00	2.4	WNW
21-Nov-2011	22:00	2.4	WNW
21-Nov-2011	23:00	2.5	NE
22-Nov-2011	0:00	2.7	NE
22-Nov-2011	1:00	2.3	NE
22-Nov-2011	2:00	2.4	NE
22-Nov-2011	3:00	2.6	E
22-Nov-2011	4:00	2.3	E
22-Nov-2011	5:00	2.3	NE
22-Nov-2011	6:00	2.1	NNE
22-Nov-2011	7:00	2.6	N
22-Nov-2011	8:00	2.9	NE
22-Nov-2011	9:00	2.7	ENE
22-Nov-2011	10:00	2.8	NNE
22-Nov-2011	11:00	3.0	NE
22-Nov-2011	12:00	2.7	E



**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

22-Nov-2011	13:00	2.8	SE
22-Nov-2011	14:00	2.9	SE
22-Nov-2011	15:00	3.1	NNE
22-Nov-2011	16:00	2.7	NE
22-Nov-2011	17:00	2.3	ENE
22-Nov-2011	18:00	2.2	ENE
22-Nov-2011	19:00	1.6	ENE
22-Nov-2011	20:00	2.2	ENE
22-Nov-2011	21:00	2.7	SSE
22-Nov-2011	22:00	2.7	ESE
22-Nov-2011	23:00	2.9	ESE
23-Nov-2011	0:00	2.6	ESE
23-Nov-2011	1:00	2.4	ESE
23-Nov-2011	2:00	2.0	ESE
23-Nov-2011	3:00	1.7	ENE
23-Nov-2011	4:00	1.8	ENE
23-Nov-2011	5:00	1.6	ENE
23-Nov-2011	6:00	1.5	NE
23-Nov-2011	7:00	1.5	NNE
23-Nov-2011	8:00	1.7	NE
23-Nov-2011	9:00	1.9	NE
23-Nov-2011	10:00	1.8	N
23-Nov-2011	11:00	1.9	W
23-Nov-2011	12:00	1.8	W
23-Nov-2011	13:00	1.9	W
23-Nov-2011	14:00	2.1	WNW
23-Nov-2011	15:00	2.5	W
23-Nov-2011	16:00	3.0	W
23-Nov-2011	17:00	3.0	NNE
23-Nov-2011	18:00	3.0	NE
23-Nov-2011	19:00	2.4	NE
23-Nov-2011	20:00	2.5	SE
23-Nov-2011	21:00	2.5	SW
23-Nov-2011	22:00	2.3	W
23-Nov-2011	23:00	2.0	WSW
24-Nov-2011	0:00	2.2	W
24-Nov-2011	1:00	2.2	W

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

24-Nov-2011	2:00	2.2	W
24-Nov-2011	3:00	2.1	S
24-Nov-2011	4:00	2.2	SSE
24-Nov-2011	5:00	2.4	E
24-Nov-2011	6:00	2.0	SE
24-Nov-2011	7:00	1.9	SE
24-Nov-2011	8:00	2.2	S
24-Nov-2011	9:00	2.0	ENE
24-Nov-2011	10:00	2.1	ESE
24-Nov-2011	11:00	2.0	S
24-Nov-2011	12:00	2.0	S
24-Nov-2011	13:00	2.1	S
24-Nov-2011	14:00	1.8	S
24-Nov-2011	15:00	1.8	ESE
24-Nov-2011	16:00	1.7	SSE
24-Nov-2011	17:00	1.5	ESE
24-Nov-2011	18:00	1.6	SSE
24-Nov-2011	19:00	1.5	SSE
24-Nov-2011	20:00	1.6	ESE
24-Nov-2011	21:00	2.1	ESE
24-Nov-2011	22:00	2.1	SSE
24-Nov-2011	23:00	2.3	E
25-Nov-2011	0:00	1.8	SE
25-Nov-2011	1:00	1.4	SSE
25-Nov-2011	2:00	1.6	SSE
25-Nov-2011	3:00	1.4	SE
25-Nov-2011	4:00	1.8	SSE
25-Nov-2011	5:00	1.9	SSE
25-Nov-2011	6:00	1.6	SSE
25-Nov-2011	7:00	2.1	SSE
25-Nov-2011	8:00	2.0	SSE
25-Nov-2011	9:00	2.3	SSE
25-Nov-2011	10:00	2.5	S
25-Nov-2011	11:00	2.5	E
25-Nov-2011	12:00	2.3	E
25-Nov-2011	13:00	2.1	E
25-Nov-2011	14:00	2.2	E

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

25-Nov-2011	15:00	2.3	E
25-Nov-2011	16:00	2.2	E
25-Nov-2011	17:00	1.8	E
25-Nov-2011	18:00	1.5	E
25-Nov-2011	19:00	1.8	E
25-Nov-2011	20:00	1.7	N
25-Nov-2011	21:00	1.7	W
25-Nov-2011	22:00	1.3	W
25-Nov-2011	23:00	1.4	WNW
26-Nov-2011	0:00	1.5	W
26-Nov-2011	1:00	1.5	W
26-Nov-2011	2:00	1.8	N
26-Nov-2011	3:00	2.2	NE
26-Nov-2011	4:00	2.0	E
26-Nov-2011	5:00	2.1	E
26-Nov-2011	6:00	2.2	NE
26-Nov-2011	7:00	2.5	E
26-Nov-2011	8:00	2.5	ESE
26-Nov-2011	9:00	2.6	SSW
26-Nov-2011	10:00	2.2	SSW
26-Nov-2011	11:00	2.6	SSW
26-Nov-2011	12:00	2.2	SSW
26-Nov-2011	13:00	2.6	NNW
26-Nov-2011	14:00	2.5	WNW
26-Nov-2011	15:00	2.4	N
26-Nov-2011	16:00	2.5	W
26-Nov-2011	17:00	2.4	S
26-Nov-2011	18:00	1.8	W
26-Nov-2011	19:00	1.8	W
26-Nov-2011	20:00	1.7	W
26-Nov-2011	21:00	2.1	W
26-Nov-2011	22:00	1.9	WSW
26-Nov-2011	23:00	2.0	W
27-Nov-2011	0:00	2.1	WNW
27-Nov-2011	1:00	1.8	W
27-Nov-2011	2:00	2.1	W
27-Nov-2011	3:00	2.1	W

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

27-Nov-2011	4:00	1.9	W
27-Nov-2011	5:00	1.8	W
27-Nov-2011	6:00	1.6	WSW
27-Nov-2011	7:00	1.6	WSW
27-Nov-2011	8:00	1.8	W
27-Nov-2011	9:00	2.3	W
27-Nov-2011	10:00	2.3	W
27-Nov-2011	11:00	2.3	SW
27-Nov-2011	12:00	2.3	ENE
27-Nov-2011	13:00	2.2	WSW
27-Nov-2011	14:00	2.2	WSW
27-Nov-2011	15:00	2.0	ESE
27-Nov-2011	16:00	2.0	W
27-Nov-2011	17:00	2.1	S
27-Nov-2011	18:00	1.7	SSW
27-Nov-2011	19:00	1.5	SSW
27-Nov-2011	20:00	1.2	SE
27-Nov-2011	21:00	1.3	SSE
27-Nov-2011	22:00	1.2	SSE
27-Nov-2011	23:00	1.6	SSE
28-Nov-2011	0:00	1.8	SSE
28-Nov-2011	1:00	1.7	SE
28-Nov-2011	2:00	1.6	SE
28-Nov-2011	3:00	1.5	SE
28-Nov-2011	4:00	1.6	ESE
28-Nov-2011	5:00	1.6	ESE
28-Nov-2011	6:00	1.7	SE
28-Nov-2011	7:00	1.7	SSE
28-Nov-2011	8:00	1.8	SSE
28-Nov-2011	9:00	1.9	ESE
28-Nov-2011	10:00	2.2	SE
28-Nov-2011	11:00	2.2	SE
28-Nov-2011	12:00	1.8	SSE
28-Nov-2011	13:00	2.0	ESE
28-Nov-2011	14:00	1.7	SSE
28-Nov-2011	15:00	1.6	SSE
28-Nov-2011	16:00	1.8	ENE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

28-Nov-2011	17:00	1.8	ENE
28-Nov-2011	18:00	1.6	SE
28-Nov-2011	19:00	1.0	ESE
28-Nov-2011	20:00	1.5	ESE
28-Nov-2011	21:00	1.6	SW
28-Nov-2011	22:00	1.4	SW
28-Nov-2011	23:00	1.9	WNW
29-Nov-2011	0:00	1.8	WSW
29-Nov-2011	1:00	1.9	W
29-Nov-2011	2:00	1.9	WNW
29-Nov-2011	3:00	2.1	WNW
29-Nov-2011	4:00	1.7	SW
29-Nov-2011	5:00	1.8	SW
29-Nov-2011	6:00	1.8	SSW
29-Nov-2011	7:00	1.4	WNW
29-Nov-2011	8:00	1.6	SW
29-Nov-2011	9:00	1.7	SW
29-Nov-2011	10:00	2.6	SW
29-Nov-2011	11:00	2.3	SW
29-Nov-2011	12:00	2.4	WSW
29-Nov-2011	13:00	2.4	SW
29-Nov-2011	14:00	2.2	SW
29-Nov-2011	15:00	2.2	WSW
29-Nov-2011	16:00	2.3	NW
29-Nov-2011	17:00	1.9	NW
29-Nov-2011	18:00	1.8	WSW
29-Nov-2011	19:00	1.8	WSW
29-Nov-2011	20:00	1.7	WSW
29-Nov-2011	21:00	1.8	S
29-Nov-2011	22:00	1.8	S
29-Nov-2011	23:00	1.6	WSW
30-Nov-2011	0:00	1.3	W
30-Nov-2011	1:00	1.4	SSW
30-Nov-2011	2:00	1.3	SW
30-Nov-2011	3:00	1.6	SW
30-Nov-2011	4:00	1.6	SSW
30-Nov-2011	5:00	1.3	SE

**APPENDIX C –  
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

**II. Mean Wind Speed and Wind Direction**

30-Nov-2011	6:00	1.1	ESE
30-Nov-2011	7:00	0.8	E
30-Nov-2011	8:00	1.0	E
30-Nov-2011	9:00	1.2	E
30-Nov-2011	10:00	1.4	E
30-Nov-2011	11:00	1.5	ENE
30-Nov-2011	12:00	1.8	W
30-Nov-2011	13:00	1.8	SW
30-Nov-2011	14:00	1.6	WNW
30-Nov-2011	15:00	1.6	WNW
30-Nov-2011	16:00	1.8	SW
30-Nov-2011	17:00	1.8	SW
30-Nov-2011	18:00	1.8	W
30-Nov-2011	19:00	2.0	WSW
30-Nov-2011	20:00	1.9	WNW
30-Nov-2011	21:00	1.7	SSW
30-Nov-2011	22:00	1.8	W
30-Nov-2011	23:00	1.9	WNW

---

---

**APPENDIX D  
ENVIRONMENTAL MONITORING  
SCHEDULES**

---

---

**Contract No. KL/2010/03**  
**Kai Tak Development - Stage 2 infrastructure works at north apron area of Kai Tak Airport for residential development**  
**and government, institution or community facilities**  
**Impact Air and Noise Monitoring Schedule for November 2011**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Nov	2-Nov	3-Nov	4-Nov	5-Nov
		1 hr TSP X3 Noise (M3(A) and M4)	Noise (M1 and M2)			24 hr TSP
6-Nov	7-Nov	8-Nov	9-Nov	10-Nov	11-Nov	12-Nov
	1 hr TSP X3 Noise (M3(A) and M4)	Noise (M1 and M2)			1 hr TSP X3 24 hr TSP	
13-Nov	14-Nov	15-Nov	16-Nov	17-Nov	18-Nov	19-Nov
	Noise (M1 and M2)			1 hr TSP X3 Noise (M3(A) and M4) 24 hr TSP		
20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov
			1 hr TSP X3 Noise (M3(A) and M4) 24 hr TSP	Noise (M1 and M2)		
27-Nov	28-Nov	29-Nov	30-Nov			
		1 hr TSP X3 Noise (M3(A) and M4) 24 hr TSP				

**Air Quality Monitoring Station**

AM1(A) - Kai Tak Operational Base  
AM2 - Lee Kau Yan Memorial School

**Noise Monitoring Station**

M1 - Buddhist Chi King Primary School  
M2 - S.K.H. Kowloon Bay Kei Lok Primary School  
M3(A) - Kai Tak Operational Base  
M4 - Lee Kau Yan Memorial School



**Contract No. KL/2010/03**  
**Kai Tak Development - Stage 2 infrastructure works at north apron area of Kai Tak Airport for residential development**  
**and government, institution or community facilities**  
**Tentative Impact Air and Noise Monitoring Schedule for December 2011**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			30-Nov	1-Dec	2-Dec	3-Dec
				Noise (M1 and M2)		
4-Dec	5-Dec	6-Dec	7-Dec	8-Dec	9-Dec	10-Dec
	1 hr TSP X3 Noise (M3(A) and M4) 24 hr TSP			Noise (M1 and M2)	1 hr TSP X3	24 hr TSP
11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec
		Noise (M1 and M2)		1 hr TSP X3 Noise (M3(A) and M4)	24 hr TSP	
18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec
			1 hr TSP X3 Noise (M3(A) and M4)	Noise (M1 and M2) 24 hr TSP		1 hr TSP X3
25-Dec	26-Dec	27-Dec	28-Dec	29-Dec	30-Dec	
			Noise (M3(A) and M4) 24 hr TSP		1 hr TSP X3 Noise (M1 and M2)	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AM1(A) - Kai Tak Operational Base  
AM2 - Lee Kau Yan Memorial School

**Noise Monitoring Station**

M1 - Buddhist Chi King Primary School  
M2 - S.K.H. Kowloon Bay Kei Lok Primary School  
M3(A) - Kai Tak Operational Base  
M4 - Lee Kau Yan Memorial School

---

---

**APPENDIX E**  
**1-HOUR TSP MONITORING RESULTS**  
**AND GRAPHICAL PRESENTATION**

---



---

## Appendix E - 1-hour TSP Monitoring Results

Location AM1(A) - Kai Tak Operational Base			
Date	Time	Weather	Particulate Concentration ( $\mu\text{g}/\text{m}^3$ )
1-Nov-11	14:00	Sunny	147.7
1-Nov-11	15:00	Sunny	145.3
1-Nov-11	16:00	Sunny	141.4
7-Nov-11	14:00	Cloudy	118.2
7-Nov-11	15:00	Cloudy	122.9
7-Nov-11	16:00	Cloudy	109.1
11-Nov-11	14:00	Cloudy	121.0
11-Nov-11	15:00	Cloudy	125.4
11-Nov-11	16:00	Cloudy	127.9
17-Nov-11	14:00	Cloudy	169.9
17-Nov-11	15:00	Cloudy	175.9
17-Nov-11	16:00	Cloudy	162.5
23-Nov-11	14:00	Cloudy	122.9
23-Nov-11	15:00	Cloudy	111.0
23-Nov-11	16:00	Cloudy	120.6
29-Nov-11	14:00	Sunny	79.7
29-Nov-11	15:00	Sunny	85.5
29-Nov-11	16:00	Sunny	91.4
Average			126.6
Maximum			175.9
Minimum			79.7

Location AM2 - Lee Kau Yan Memorial School			
Date	Time	Weather	Particulate Concentration ( $\mu\text{g}/\text{m}^3$ )
1-Nov-11	14:00	Sunny	140.1
1-Nov-11	15:00	Sunny	129.5
1-Nov-11	16:00	Sunny	125.2
7-Nov-11	14:00	Cloudy	104.0
7-Nov-11	15:00	Cloudy	115.8
7-Nov-11	16:00	Cloudy	121.7
11-Nov-11	14:00	Cloudy	120.0
11-Nov-11	15:00	Cloudy	123.9
11-Nov-11	16:00	Cloudy	126.6
17-Nov-11	14:00	Cloudy	153.5
17-Nov-11	15:00	Cloudy	149.0
17-Nov-11	16:00	Cloudy	158.2
23-Nov-11	14:00	Cloudy	147.9
23-Nov-11	15:00	Cloudy	135.7
23-Nov-11	16:00	Cloudy	127.2
29-Nov-11	14:00	Sunny	137.5
29-Nov-11	15:00	Sunny	142.1
29-Nov-11	16:00	Sunny	144.5
Average			133.5
Maximum			158.2
Minimum			104.0

## 1-hr TSP Concentration Levels

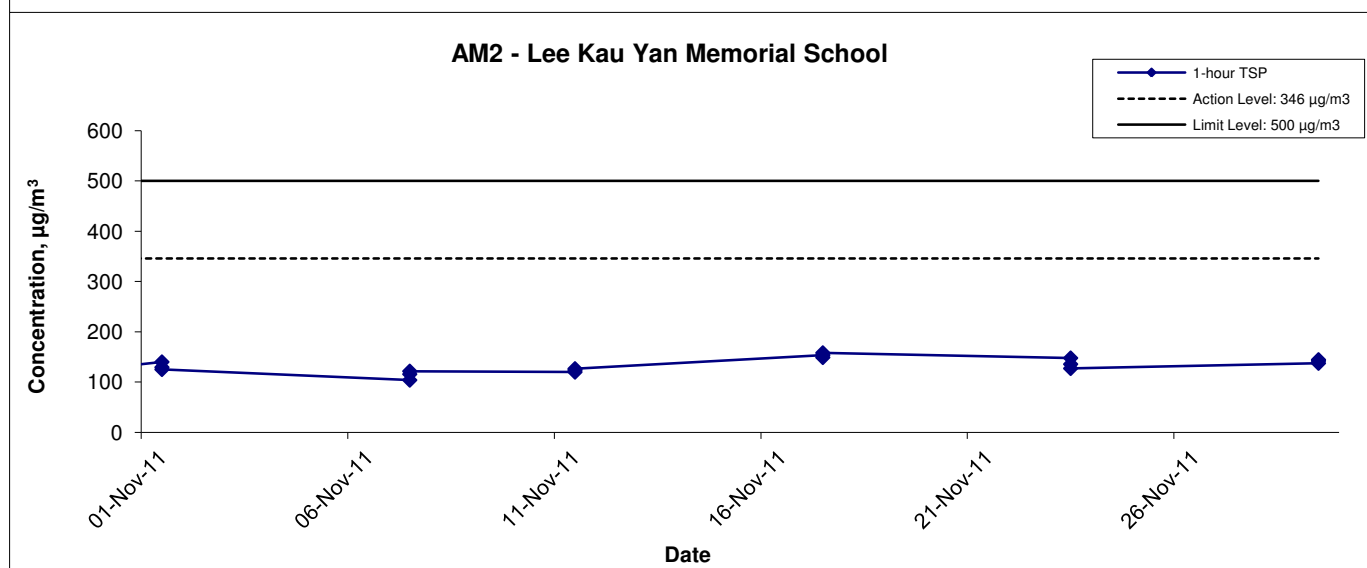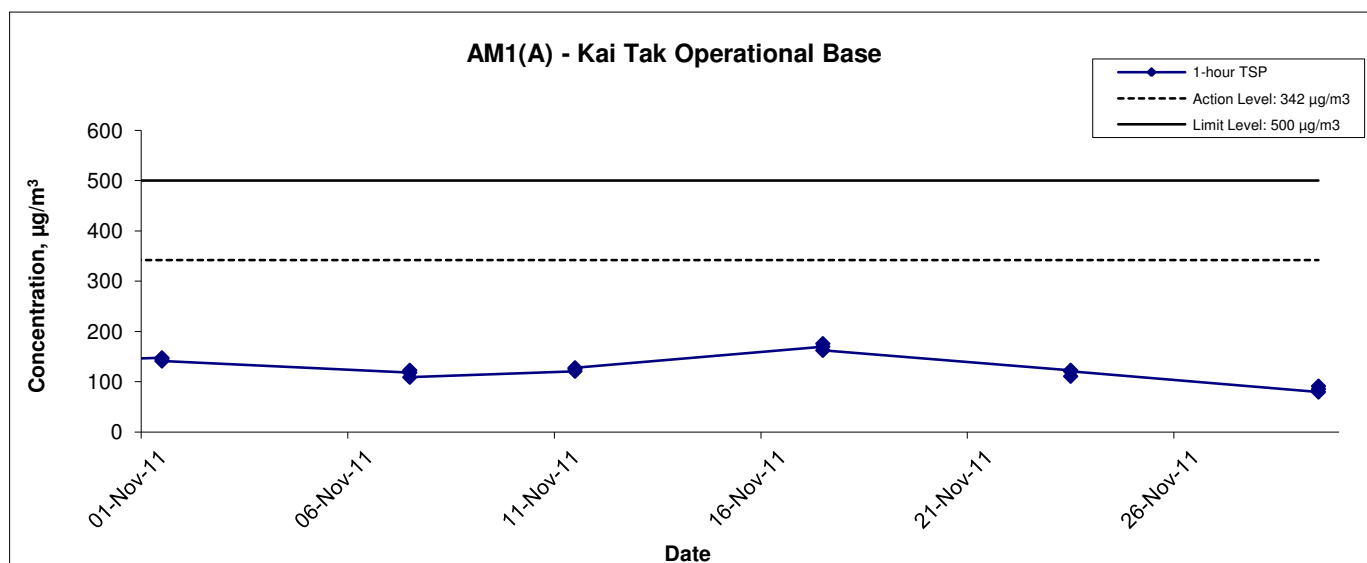

<b>Title</b> EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD  Graphical Presentation of 1-hour TSP Monitoring Results	<b>Scale</b> N.T.S	<b>Project No.</b> MA11038	
	<b>Date</b> Nov 11	<b>Appendix</b> E	

---

---

**APPENDIX F**  
**24-HOUR TSP MONITORING RESULTS**  
**AND GRAPHICAL PRESENTATION**

---

---

## Appendix F - 24-hour TSP Monitoring Results


### Location AM1(A) - Kai Tak Operational Base

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
5-Nov-11	Sunny	300.2	764.3	3.4721	3.5921	0.1200	1753.0	1777.0	24.0	1.22	1.22	1.22	1763.1	68.1
11-Nov-11	Cloudy	298.2	766.1	3.4148	3.5674	0.1526	1777.0	1801.0	24.0	1.23	1.23	1.23	1771.1	86.2
17-Nov-11	Cloudy	296.7	763.6	3.4227	3.5852	0.1625	1801.0	1825.0	24.0	1.23	1.23	1.23	1772.7	91.7
23-Nov-11	Cloudy	293.5	769.1	3.4135	3.4954	0.0819	1825.0	1849.0	24.0	1.24	1.24	1.24	1788.9	45.8
29-Nov-11	Sunny	296.6	765.1	3.4082	3.4506	0.0424	1849.0	1873.0	24.0	1.23	1.23	1.23	1774.7	23.9
													Min	23.9
													Max	91.7
													Average	63.1

### Location AM2 - Lee Kau Yan Memorial School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
5-Nov-11	Sunny	300.2	764.3	3.4465	3.5219	0.0754	1657.0	1681.0	24.0	1.21	1.21	1.21	1739.1	43.4
11-Nov-11	Cloudy	298.2	766.1	3.4096	3.5818	0.1722	1681.0	1705.0	24.0	1.21	1.21	1.21	1747.3	98.6
17-Nov-11	Cloudy	296.7	763.6	3.4118	3.6019	0.1901	1705.0	1729.0	24.0	1.21	1.21	1.21	1748.9	108.7
23-Nov-11	Cloudy	293.5	769.1	3.4085	3.5233	0.1148	1729.0	1753.0	24.0	1.23	1.23	1.23	1765.2	65.0
29-Nov-11	Sunny	296.6	765.1	3.0748	3.2093	0.1345	1753.0	1777.0	24.0	1.22	1.22	1.22	1750.9	76.8
													Min	43.4
													Max	108.7
													Average	78.5

## 24-hr TSP Concentration Levels

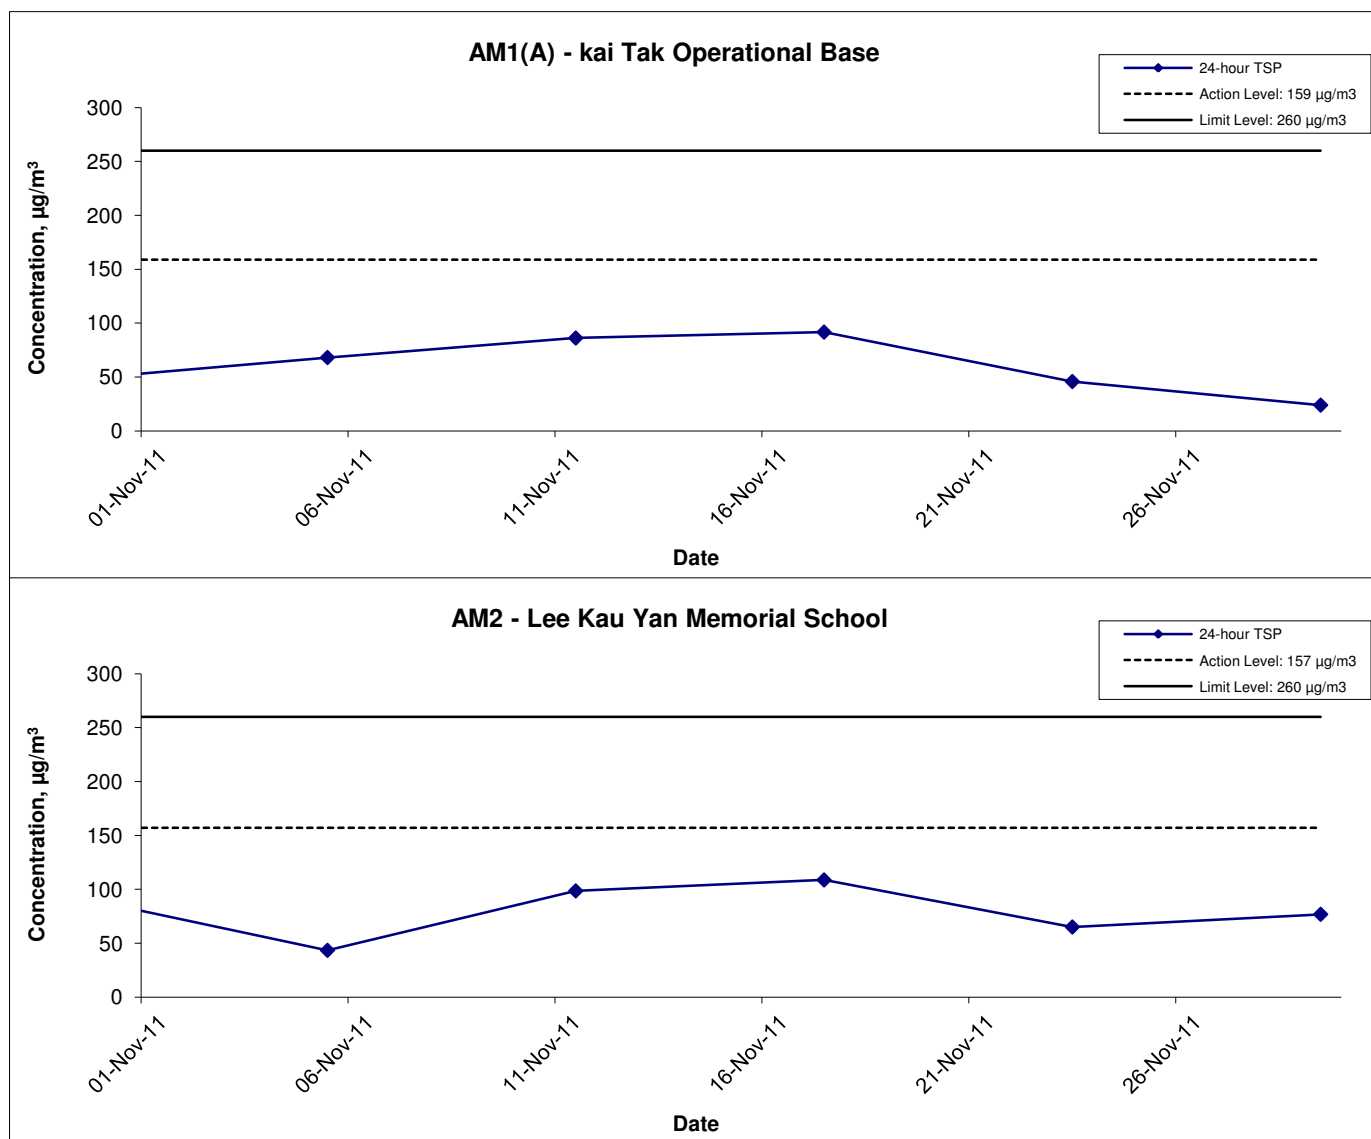

Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD		Scale	N.T.S	Project No.	MA11038	CINOTECH
	Graphical Presentation of 24-hour TSP Monitoring Results		Date	Nov 11	Appendix	F	

---

**APPENDIX G**  
**NOISE MONITORING RESULTS AND**  
**GRAPHICAL PRESENTATION**

---



## Appendix G - Noise Monitoring Results




Location M1 - Buddhist Chi King Primary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
2-Nov-11	14:00	Sunny	65.8	67.6	63.4	64.4	60.2
8-Nov-11	14:00	Cloudy	66.4	68.8	63.5		62.1
14-Nov-11	14:00	Sunny	64.2	67.4	60.5		64.2
24-Nov-11	14:00	Sunny	66.7	68.2	63.3		62.8

Location M2 - S.K.H. Kowloon Bay Kei Lok Primary School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
2-Nov-11	15:00	Sunny	65.8	68.0	62.8	61.3	63.9
8-Nov-11	15:00	Cloudy	65.5	67.7	62.5		63.4
14-Nov-11	15:00	Sunny	65.8	67.3	64.3		63.9
24-Nov-11	15:00	Sunny	67.3	70.7	63.6		66.0

Location M3(A) - Kai Tak Operational Base							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
1-Nov-11	14:00	Sunny	65.2	67.2	62.0	65.8	65.2 Measured $\leq$ Baseline
7-Nov-11	14:00	Cloudy	65.9	67.6	62.2		49.5
17-Nov-11	14:00	Cloudy	66.5	68.1	62.6		58.2
23-Nov-11	14:00	Cloudy	67.4	68.7	63.5		62.3
29-Nov-11	14:00	Sunny	64.7	66.8	61.8		64.7 Measured $\leq$ Baseline


Location M4 - Lee Kau Yan Memorial School							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
1-Nov-11	15:00	Sunny	75.6	77.3	72.0	76.7	75.6 Measured $\leq$ Baseline
7-Nov-11	15:00	Cloudy	73.5	75.5	71.8		73.5 Measured $\leq$ Baseline
17-Nov-11	15:00	Cloudy	73.1	74.7	71.9		73.1 Measured $\leq$ Baseline
23-Nov-11	15:00	Cloudy	72.5	73.6	71.6		72.5 Measured $\leq$ Baseline
29-Nov-11	15:00	Sunny	76.5	78.0	74.8		76.5 Measured $\leq$ Baseline

## Noise Levels

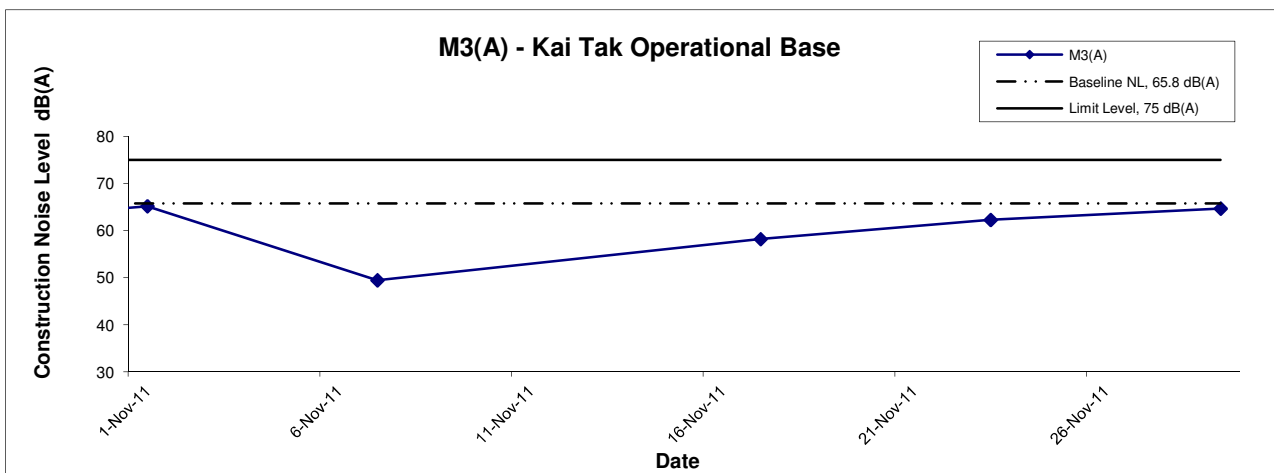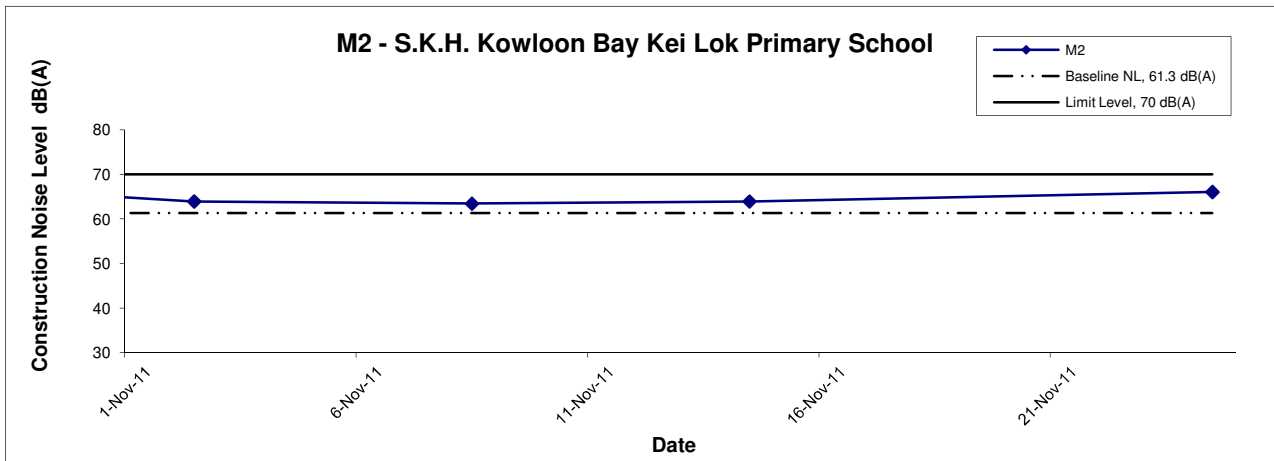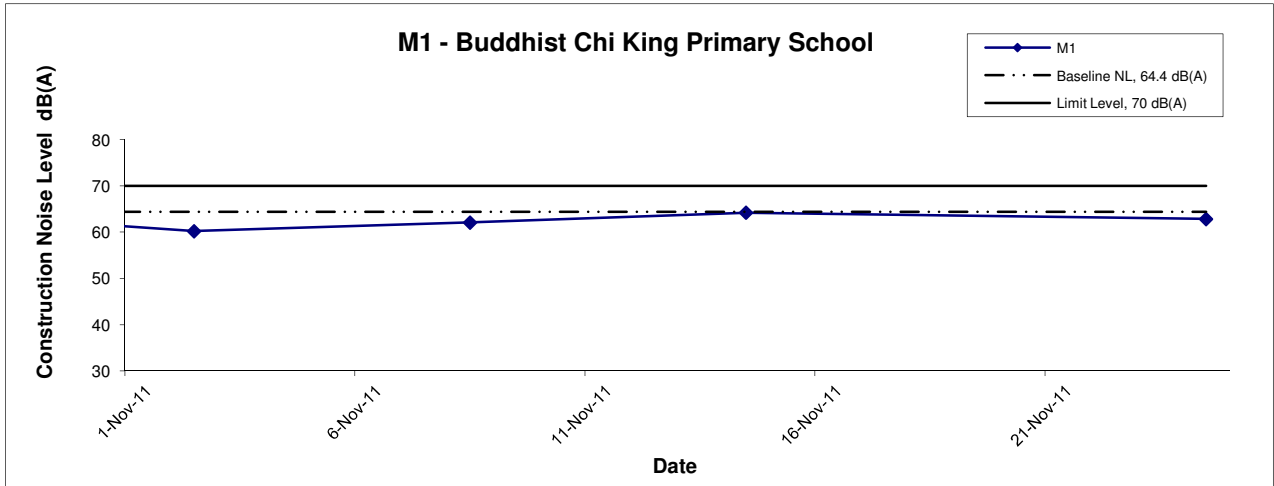

Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD	Scale	N.T.S	Project No.	MA11038	CINOTECH
	Graphical Presentation of Construction Noise Monitoring Results	Date	Nov 11	Appendix	G	

## Noise Levels

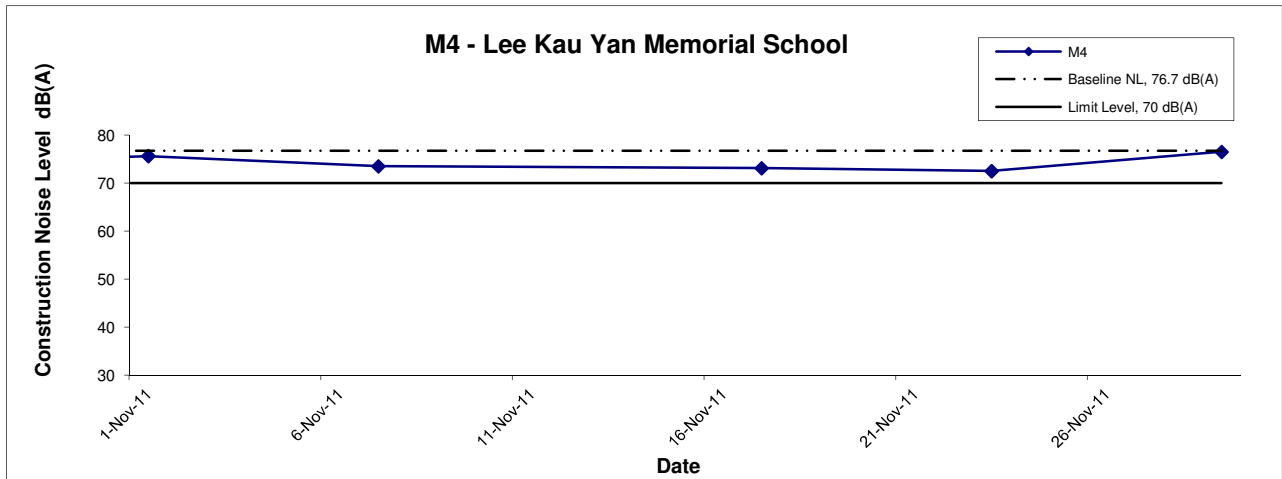

Title	EP-344/2009 – New Sewage Pumping Stations Serving KTD and EP-337/2009 – New Distributor Roads Serving the Planned KTD		Scale	Project No.	CINOTECH
	Graphical Presentation of Construction Noise Monitoring Results		N.T.S	MA11038	
			Date	Appendix	
			Nov 11	G	

---

---

**APPENDIX H**  
**SUMMARY OF EXCEEDANCE**

---

---

**EP-344/2009 – New Sewage Pumping Stations Serving KTD and  
EP-337/2009 – New Distributor Roads Serving the Planned KTD**

**Appendix H – Summary of Exceedance (November 2011)**

**Exceedance Report**

- (A) Exceedance Report for Air Quality  
(NIL in the reporting month)**
- (B) Exceedance Report for Construction Noise  
(NIL in the reporting month)**
- (C) Exceedance Report for Landscape and Visual  
(NIL in the reporting month)**

---

**APPENDIX I**  
**SITE AUDIT SUMMARY**

---



Contract No. KL/2010/03

**Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities, Kai Tak Development – Stage 2**

**Weekly Site Inspection Record Summary**  
**Inspection Information**

Checklist Reference Number	111103
Date	3 November 2011
Time	9:30 – 10:45

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>B. Air Quality</b>	
111103-R02	<u>Reminder:</u> • To provide water spray for the exposed site area and during breaking works at stockpiling site.	C5, 6 & 13
	<b>C. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Waste / Chemical Management</b>	
111103-R01	<u>Reminder:</u> • To clear the chemical oil at the drip tray and oil spillage at PS1A properly.	E8 & 9
	<b>E. Visual and Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Others</b>	
	• Follow-up on previous site audit session (Ref. No. 111027), all environmental deficiencies were improved/ rectified by the Contractor.	

	Name	Signature	Date
Recorded by	Ivy Tam		3 November 2011
Checked by	Dr. Priscilla Choy		3 November 2011



Contract No. KL/2010/03

**Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities, Kai Tak Development – Stage 2**

**Weekly Site Inspection Record Summary**  
**Inspection Information**

Checklist Reference Number	111110
Date	10 November 2011
Time	14:00 – 15:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
111110-R01	• To clear the stagnant mud water after relevant construction of site PS1A is done.	B8
	<b>B. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Visual and Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Others</b>	
	• Follow-up on previous site audit session (Ref. No. 111103), all environmental deficiencies were improved/ rectified by the Contractor.	

	Name	Signature	Date
Recorded by	Ivy Tam		10 November 2011
Checked by	Dr. Priscilla Choy		10 November 2011





Contract No. KL/2010/03

**Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities, Kai Tak Development – Stage 2**

**Weekly Site Inspection Record Summary**  
**Inspection Information**

Checklist Reference Number	111115
Date	15 November 2011
Time	09:45 – 10:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
111115-R02	• The contractor is reminded to turn on the pump and remove the stagnant water at box culvert BC6.	B8
	<b>B. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Noise</b>	
111115-R01	• To provide valid noise label for the air compressor at the box culvert BC6.	D8
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Visual and Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Others</b>	
111115-R03	• <u>Remarks:</u> To store the wooden boards in tidy manner. • Follow-up on previous site audit session (Ref. No. 111110), all environmental deficiencies were improved/ rectified by the Contractor.	E4ii

	Name	Signature	Date
Recorded by	Ivy Tam		15 November 2011
Checked by	Dr. Priscilla Choy		15 November 2011

Contract No. KL/2010/03



**Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities, Kai Tak Development – Stage 2**

**Weekly Site Inspection Record Summary**

**Inspection Information**

Checklist Reference Number	111124
Date	24 November 2011
Time	09:30 – 11:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>B. Air Quality</b>	
111124-R01	• To provide water spray for the exposed site area (Box Culvert BC6) more frequently.	C5, 6 & 13
	<b>C. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Waste / Chemical Management</b>	
111124-R02	• To provide drip tray for the oil drum at Box Culvert BC6.	E9
	<b>E. Visual and Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Others</b>	
	• Follow-up on previous site audit session (Ref. No. 111115), all environmental deficiencies were improved/ rectified by the Contractor.	

	Name	Signature	Date
Recorded by	Ivy Tam		24 November 2011
Checked by	Dr. Priscilla Choy		24 November 2011

---

**APPENDIX J**  
**EVENT ACTION PLANS**

---

## Appendix J - Event Action Plans

### Event/Action Plan for Air Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contactor, IEC and ER;</li> <li>3. Repeat measurement to confirm finding.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Action Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contractor, IEC and ER;</li> <li>3. Increase monitoring frequency to daily;</li> <li>4. Discuss with IEC and Contractor on remedial actions required;</li> <li>5. Assess the effectiveness of Contractor's remedial actions;</li> <li>6. If exceedance continues, arrange meeting with IEC and ER;</li> <li>7. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise implementation of remedial measures;</li> <li>5. Conduct meeting with ET and IEC if exceedance continues.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET and IEC on proper remedial actions;</li> <li>2. Submit proposals for remedial actions to ER and IEC within three working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Amend proposal if appropriate.</li> </ol>
Limit Level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Inform Contractor, IEC, ER, and EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Assess effectiveness of Contractor's remedial actions and keep</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Discuss with ET and IEC on proper remedial actions;</li> <li>3. Submit proposals for remedial actions to ER and IEC within three</li> </ol>

## Appendix J - Event Action Plans

	EPD, IEC and ER informed of the results.	4. Advise the ER on the effectiveness of the proposed remedial measures.	implemented; 4. Supervise implementation of remedial measures; 5. Conduct meeting with ET and IEC if exceedance continues.	working days of notification; 4. Implement the agreed proposals.
Limit Level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Notify IEC, ER, Contractor and EPD;</li> <li>2. Repeat measurement to confirm findings;</li> <li>3. Carry out analysis of Contractor's working procedures to identify source and investigate the causes of exceedance;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Arrange meeting with IEC, ER and Contractor to discuss the remedial actions to be taken;</li> <li>6. Assess effectiveness of Contractor's remedial actions and keep EPD, IEC and ER informed of the results;</li> <li>7. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Discuss with ET, ER and IEC on proper remedial actions;</li> <li>3. Submit proposals for remedial actions to IEC within three working days of notification;</li> <li>4. Implement the agreed proposals;</li> <li>5. Submit further remedial actions if problem still not under control;</li> <li>6. Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> </ol>

## Appendix J - Event Action Plans

### Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)
Limit Level being exceeded	1. Inform IEC, ER, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance;	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals;

## Appendix J - Event Action Plans

	<p>5. Carry out analysis of Contractor's working procedures;</p> <p>6. Discuss with the IEC, Contractor and ER on remedial measures required;</p> <p>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring.</p> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<p>measures to be implemented;</p> <p>4. Supervise the implementation of remedial measures;</p> <p>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</p> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<p>4. Submit further proposal if problem still not under control;</p> <p>5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</p> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>
--	---	---	---	--

## Appendix J - Event Action Plans

### Event/Action Plan for Landscape and Visual

EVENT ACTION LEVEL	ACTION			
	ET	IEC	ER	CONTRACTOR
Design Check	1. Check final design conforms to the requirements of EP and prepare report.	1. Check report. 2. Recommend remedial design if necessary	1. Undertake remedial design if necessary	
Non-conformity on one occasion	1. Identify Source 2. Inform IEC and ER 3. Discuss remedial actions with IEC, ER and Contractor 4. Monitor remedial actions until rectification has been completed	1. Check report 2. Check Contractor's working method 3. Discuss with ET and Contractor on possible remedial measures 4. Advise ER on effectiveness of proposed remedial measures. 5. Check implementation of remedial measures.	1. Notify Contractor 2. Ensure remedial measures are properly implemented	1. Amend working methods 2. Rectify damage and undertake any necessary replacement
Repeated Non-conformity	1. Identify Source Inform IEC and	1. Check monitoring report	1. Notify Contractor 2. Ensure remedial measures are properly	1. Amend working methods 2. Rectify damage and



## Appendix J - Event Action Plans

	ER 2. Increase monitoring frequency 3. Discuss remedial actions with IEC, ER and Contractor 4. Monitor remedial actions until rectification has been completed 5. If non-conformity stops, cease additional monitoring	2. Check Contractor's working method 3. Discuss with ET and Contractor on possible remedial measures 4. Advise ER on effectiveness of proposed remedial measures 5. Supervise implementation of remedial measures.	implemented	undertake any necessary replacement
--	--	---	-------------	-------------------------------------

---

**APPENDIX K  
ENVIRONMENTAL MITIGATION  
IMPLEMENTATION SCHEDULE (EMIS)**

---

## Appendix K - Summary of Implementation Schedule of Mitigation Measures for Construction Phase

Types of Impacts	Mitigation Measures	Status
Construction Dust	8 times daily watering of the work site with active dust emitting activities.	*
	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimize cumulative dust impacts.	
	<ul style="list-style-type: none"> <li>Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.</li> </ul>	*
	<ul style="list-style-type: none"> <li>Misting for the dusty material should be carried out before being loaded into the vehicle.</li> </ul>	*
	<ul style="list-style-type: none"> <li>Any vehicle with an open load carrying area should have properly fitted side and tail boards.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.</li> </ul>	*
	<ul style="list-style-type: none"> <li>The tarpaulin should be properly secured and should extend at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation.</li> </ul>	*
	<ul style="list-style-type: none"> <li>The vehicles should be restricted to maximum speed of 10 km per hour and confined haulage and delivery vehicle to designated roadways insider the site. On-site unpaved roads should be compacted and kept free of lose materials.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Vehicle washing facilities should be provided at every</li> </ul>	^

	<p>vehicle exit point.</p> <ul style="list-style-type: none"> <li>• The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> <li>• Every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.</li> <li>• Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the three sides.</li> <li>• Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.</li> <li>• <u>DWFI compound for JVBC</u>: a DWFI compound is proposed at the downstream of JVC to contain pollution in drainage systems entering the KTAC and KTTS by interception facilities until the ultimate removal of the pollution sources. Tidal barriers and desilting facilities will form part of the compounds to prevent any accumulation of sediment within the downstream section of JVBC and hence fully mitigate the potential odour emissions from the headspace of JVBC near the existing discharge locations. The odour generating operations within the proposed desilting compound will be fully enclosed and the odorous air will be collected and treated by high</li> </ul>	<p>^</p> <p>^</p> <p>*</p> <p>^</p> <p>N/A</p>
--	---	--

	<p>efficiency deodorizers before discharge to the atmosphere.</p> <ul style="list-style-type: none"> <li>• <u>Desilting compound for KTN:</u> Two desilting compounds are proposed for KTN (at Site 1D6 and Site 1P1) to contain pollution in drainage systems entering the KTAC and KTTS by interception facilities until the ultimate removal of the pollution sources. Tidal barriers and desilting facilities will form part of the compounds to prevent any accumulation of sediment within the downstream section of KTN and hence fully mitigate the potential odour emissions from the headspace of KTN near the existing discharge locations. The odour generating operations within the proposed desilting compound will be fully enclosed and the odorous air will be collected and treated by high efficiency deodorizers before discharge to the atmosphere.</li> <li>• <u>Decking or reconstruction of KTN within apron area:</u> it is proposed to deck the KTN or reconstruct the KTN within the former Apron area into Kai Tak River from the south of Road D1 to the north of Road D2 along the existing alignment of KTN. The Kai Tak River will compose of a number of channels flowing with non-odorous fresh water and THEES effluent. The channel flowing with THEES effluent will be designed with the width of water surface of not more than 16m.</li> </ul>	<p>N/A</p> <p>N/A</p>
--	--	-----------------------



	<ul style="list-style-type: none"> <li>● <u>Localised maintenance dredging:</u> Localised maintenance dredging should be conducted to provide water depth of not less than 3.5m over the whole of KTAC and KTTS. With reference to the water depth data recorded during the odour survey, only some of the areas in the northern part of KTAC (i.e. to the north of taxiway bridge) including the area near the northern edge of KTAC, the area near western bank of KTAC, and the area near the JVC discharge have water depths shallower than 3.5m. The area involved would be about 40% of the northern KTAC and the dredging depth required would be from about 2.7m to less than 1m. The maintenance dredging to be carried out prior to the occupation of any new development in the immediate vicinity of KTAC to avoid potential localized odour impacts at the future ASRs during the maintenance dredging operation.</li> <li>● <u>Improvement of water circulation in KTAC and KTTS:</u> 600m gap opening at the northern part of the former Kai Tak runway, the water circulation in KTAC and KTTS would be substantially improved. Together with the improvement in water circulation, the DO level in KTAC and KTTS would also be increased.</li> <li>● <u>In-situ sediment treatment by bioremediation:</u> Bioremediation would be applied to the entire KTAC and KTTS.</li> </ul>	<p>^</p> <p>N/A</p> <p>N/A</p>
--	--	--------------------------------

Construction Noise	Use of quiet PME, movable barriers barrier for Asphalt Paver, Breaker, Excavator and Hand-held breaker and full enclosure for Air Compressor, Bar Bender, Concrete Pump, Generator and Water Pump	^
	Good Site Practice:	^
	<ul style="list-style-type: none"> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.</li> <li>Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program.</li> <li>Mobile plant, if any, should be sited as far away from NSRs as possible.</li> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	N/A(1)
	Scheduling of Construction Works during School Examination Period	^
	(i) Provision of low noise surfacing in a section of Road L2; and	N/A
	(ii) Provision of structural fins	N/A

	(i) Avoid the sensitive façade of class room facing Road L2 and L4; and	N/A
	(ii) Provision of low noise surfacing in a section of Road L2 & L4	N/A
	(i) Provision of low noise surfacing in a section of Road L4 before occupation of Site 1I1; and	N/A
	(ii) Setback of building about 5m from site boundary.	N/A
	Setback of building about 35m to the northwest direction at 1L3 and 5m at Site 1L2.	N/A
	(i) avoid any sensitive façades with openable window facing the existing Kowloon City Road network; and	N/A
	(ii) for the sensitive facades facing the To Kwa Wan direction, either setback the facades by about 5m to the northeast direction or do not provide the facades with openable window.	N/A
	(i) avoid any sensitive facades with openable window facing the existing To Kwa Wan Road or	N/A
	(ii) provision of 17.5m high noise tolerant building fronting To Kwa Wan Road and restrict the height of the residential block(s) located at less than 55m away from To Kwa Wan Road to no more than 25m above ground.	N/A
	(i) avoid any sensitive facades with openable window facing the slip road connecting Prince Edward Road East and San Po Kong or other alternative mitigation measures and at-source mitigation measures for the surrounding new local roads to minimise the potential traffic noise impacts from the slip road	N/A



	<p>All the ventilation fans installed in the below will be provided with silencers or acoustics treatment.</p> <ul style="list-style-type: none"> <li>(i) SPS</li> <li>(ii) ESS</li> <li>(iii) Tunnel Ventilation Shaft</li> <li>(iv) EFTS depot</li> </ul> <p>Installation of retractable roof or other equivalent measures</p>	<p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p>
--	--	--

<p><b>Construction Water Quality</b></p>	<p>The following mitigation measures are proposed to be incorporated in the design of the SPS at KTD, including:</p> <ul style="list-style-type: none"> <li>• Dual power supply or emergency generator should be provided at all the SPSs to secure electrical power supply;</li> <li>• Standby pumps should be provided at all SPSs to ensure smooth operation of the SPS during maintenance of the duty pumps;</li> <li>• An alarm should be installed to signal emergency high water level in the wet well at all SPSs; and</li> <li>• For all unmanned SPSs, a remote monitor system connecting SPSs with the control station through telemetry system should be provided so that swift actions could be taken in case of malfunction of unmanned facilities.</li> </ul> <p><b>Construction Phase</b>  <u>Marine-based Construction</u></p> <p><i>Capital and Maintenance Dredging for Cruise Terminal</i></p> <p>Mitigation measures for construction of the proposed cruise terminal should follow those recommended in the approved EIA for CT Dredging.</p>	<p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>^</p>
--	---	--

	<p><i>Fireboat Berth, Runway Opening and Road T2</i></p> <p>Silt curtains should be deployed around the close grab dredger to minimize release of sediment and other contaminants for any dredging and filling activities in open water.</p> <p>Dredging at and near the seawall area for construction of the public landing steps cum fireboat berth should be carried out at a maximum production rate of 1,000m<sup>3</sup> per day using one grab dredger.</p> <p>The proposed construction method for runway opening should adopt an approach where the existing seawall at the runway will not be removed until completion of all excavation and dredging works for demolition of the runway. Thus, excavation of bulk fill and majority of the dredging works will be carried out behind the existing seawall, and the sediment plume can be effectively contained within the works area. As there is likely some accumulation of sediments alongside the runway, there will be a need to dredge the existing seabed after completion of all the demolition works. Dredging alongside the 600m opening should be carried out at a maximum production rate of 2,000m<sup>3</sup> per day using one grab dredger.</p> <p>Dredging for Road T2 should be conducted at a maximum rate of 8,000m<sup>3</sup> per day (using four grab dredgers) whereas the sand filling should be conducted at a maximum rate of 2,000m<sup>3</sup> per day (using two grab dredgers).</p> <p>Silt screens shall be applied to seawater intakes at WSD seawater intake.</p>	<p>*</p> <p>^</p> <p>^</p> <p>N/A (1)</p> <p>^</p>
--	--	--

	<p><u>Land-based Construction</u></p> <p><i>Construction Runoff</i></p> <p>Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include:</p> <ul style="list-style-type: none"> <li>• use of sediment traps</li> <li>• adequate maintenance of drainage systems to prevent flooding and overflow</li> </ul> <p>Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.</p>	<p>*</p> <p>*</p> <p>*</p>
--	---	----------------------------



	<p>Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.</p> <p>Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m<sup>3</sup> capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.</p> <p>Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m<sup>3</sup> should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.</p> <p>Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p>
--	---	-------------------------------------

	<p>Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.</p> <p>Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.</p> <p>All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.</p> <p><i>Drainage</i></p> <p>It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p>
--	--	-------------------------------------

	<p>All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.</p> <p>All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ.</p> <p><i>Sewage Effluent</i></p> <p>Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.</p> <p><i>Stormwater Discharges</i></p> <p>Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p>
--	---	-------------------------------------



	<p><i>Debris and Litter</i></p> <p>In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur</p> <p><i>Construction Works at or in Close Proximity of Storm Culvert or Seafront</i></p> <p>The proposed works should preferably be carried out within the dry season where the flow in the drainage channel /storm culvert/ nullah is low.</p> <p>The use of less or smaller construction plants may be specified to reduce the disturbance to the bottom sediment at the drainage channel /storm culvert / nullah.</p> <p>Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</p> <p>Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</p> <p>Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</p> <hr/> <p>Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>*</p> <p>*</p> <p>^</p>
--	--	--



	<p>Mitigation measures to control site runoff from entering the nearby water environment should be implemented to minimize water quality impacts. Surface channels should be provided along the edge of the waterfront within the work sites to intercept the runoff.</p>	*
	<p>Construction effluent, site run-off and sewage should be properly collected and/or treated.</p>	*
	<p>Any works site inside the storm water courses should be temporarily isolated, such as by placing of sandbags or silt curtains with lead edge at bottom and properly supported props to prevent adverse impact on the storm water quality.</p>	*
	<p>Silt curtain may be installed around the construction activities at the seafront to minimize the potential impacts due to accidental spillage of construction materials.</p>	^
	<p>Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert/drainage channel/sea.</p>	*
	<p>Supervisory staff should be assigned to station on site to closely supervise and monitor the works</p>	^
	<p>Marine water quality monitoring and audit programme shall be implemented for the proposed sediment treatment operation.</p>	^

	<p>Good Site Practices</p> <p>It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are adhered to. Recommendations for good site practices during construction activities include:</p> <ul style="list-style-type: none"> <li>• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>• Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>• Provision of sufficient waste disposal points and regular collection for disposal</li> <li>• Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers</li> <li>• A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites)</li> </ul>	<p>^</p> <p>*</p> <p>*</p> <p>*</p> <p>^</p>
--	---	--

	<p><b>Waste Reduction Measures</b></p> <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>• Sort C&amp;D waste from demolition of the remaining structures to recover recyclable portions such as metals</li> <li>• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal</li> <li>• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force</li> <li>• Any unused chemicals or those with remaining functional capacity should be recycled</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials</li> </ul> <p><b>Dredged Marine Sediment</b></p> <p>The basic requirements and procedures for dredged mud disposal are specified under the ETWB TCW No. 34/2002. The management of the dredging, use and disposal of marine mud is monitored by the MFC, while the licensing of marine dumping is required under the Dumping at Sea Ordinance and is the responsibility of the Director of Environmental Protection (DEP)</p>	<p>*</p> <p>*</p> <p>*</p> <p>^</p> <p>*</p> <p>^</p>
--	---	---

	<p>The dredged marine sediments would be loaded onto barges and transported to the designated disposal sites allocated by the MFC depending on their level of contamination. Sediment classified as Category L would be suitable for Type 1 - Open Sea Disposal. Contaminated sediment would require either Type 1 – Open Sea Disposal (Dedicated Sites), Type 2 - Confined Marine Disposal, or Type 3 – Special Treatment / Disposal and must be dredged and transported with great care in accordance with ETWB TCW No. 34/2002. Subject to the final allocation of the disposal sites by MFC, the dredged contaminated sediment must be effectively isolated from the environment and disposed properly at the designated disposal site</p>	<p>^</p>
--	--	----------



	<p>It will be the responsibility of the contractor to satisfy the appropriate authorities that the contamination levels of the marine sediment to be dredged have been analysed and recorded. According to the ETWB TCW No. 34/2002, this will involve the submission of a formal Sediment Quality Report to the DEP, prior to the dredging contract being tendered. The contractor for the dredging works should apply for allocation of marine disposal sites and all necessary permits from relevant authorities for the disposal of dredged sediment. During transportation and disposal of the dredged marine sediments requiring Type 1, Type 2, or Type 3 disposal, the following measures should be taken to minimise potential impacts on water quality:</p> <ul style="list-style-type: none"> <li>• Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved</li> <li>• Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as required under the Dumping at Sea Ordinance and as specified by the DEP</li> <li>• Barges or hopper barges should not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation</li> </ul>	<p>^</p> <p>^</p> <p>^</p>
--	---	----------------------------

	<p><b>Construction and Demolition Material</b></p> <p>Mitigation measures and good site practices should be incorporated into contract document to control potential environmental impact from handling and transportation of C&amp;D material. The mitigation measures include:</p> <ul style="list-style-type: none"> <li>• Where it is unavoidable to have transient stockpiles of C&amp;D material within the Project work site pending collection for disposal, the transient stockpiles should be located away from waterfront or storm drains as far as possible</li> <li>• Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric</li> <li>• Skip hoist for material transport should be totally enclosed by impervious sheeting</li> <li>• Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site</li> <li>• The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores</li> <li>• The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle</li> <li>• All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet</li> <li>• The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading</li> </ul>	<p>^</p> <p>*</p> <p>*</p> <p>^</p> <p>^</p> <p>^</p> <p>*</p> <p>*</p>
--	--	---

	<p>When delivering inert C&amp;D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&amp;D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Materials" should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.</p> <p>Chemical Waste</p> <p>After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i></p> <p>General Refuse</p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&amp;D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&amp;D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem</p>	<p>^</p> <p>^</p> <p>*</p>
--	---	----------------------------



<p><b>Landscape and Visual</b></p>	<p>CM1 All existing trees should be carefully protected during construction.</p> <p>CM2 Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.</p> <p>CM3 Control of night-time lighting.</p> <p>CM4 Erection of decorative screen hoarding.</p>	<p>^</p> <p>^</p> <p>N/A(1)</p> <p>^</p>
------------------------------------	---	--

Remarks:	^ Compliance of mitigation measure;	X Non-compliance of mitigation measure;
	N/A Not Applicable at this stage; N/A(1) Not observed;	•Non-compliance but rectified by the contractor;
	* Recommendation was made during site audit but improved/rectified by the contractor.	



---

**APPENDIX L  
SUMMARIES OF ENVIRONMENTAL  
COMPLAINT, WARNING, SUMMON  
AND NOTIFICATION OF SUCCESSFUL  
PROSECUTION**

---

**EP-344/2009 – New Sewage Pumping Stations Serving KTD and  
EP-337/2009 – New Distributor Roads Serving the Planned KTD**

**Appendix L – Summary of environmental complaint, warning, summon and notification of  
successful prosecution**

**Reporting Month:** November 2011

**Contract No.** KL/2010/03

<b>Log Ref.</b>	<b>Location</b>	<b>Received Date</b>	<b>Details of Complaint/warning/summon and prosecution</b>	<b>Investigation/Mitigation Action</b>	<b>Status</b>
N/A	N/A	N/A	N/A	N/A	N/A

**Remarks:** No environmental complaint/warning/summon and prosecution were received in the reporting period.

---

---

**APPENDIX M**  
**WASTE GENERATED QUANTITY**

---

---

Department: CEDD  
Contract No.: KL/2010/03  
Project : KAI TAK DEVELOPMENT – STAGE 2 Infrastructure Works at North Apron Area of Kai Tak Airport for Residential Development and Government Facilities



### Monthly Summary Waste Flow Table

As at 10 Dec 2011

Month	Total Quantity Generated (in m <sup>3</sup> )	Actual Quantities Inert C & D Materials Generated Monthly					Actual Quantities of C & D Wastes Generated Monthly					
		Broken Concrete (See Note 3) (in m <sup>3</sup> )	Reused in the Contract (in m <sup>3</sup> )	Reused in other Projects (in m <sup>3</sup> )	Disposed as Public Fill (in m <sup>3</sup> )	Imported Fill (in m <sup>3</sup> )	Metals (in kg)	Paper/ Cardboard packaging (in kg)	Plastics (see Note 2) (in kg)	Chemical Waste		Others, e.g. general refuse (in m <sup>3</sup> )
										Battery(No.)	Oil(in L)	
Jul'2011	0	0	0	0	0	0	0	0	0	0	0	0
Aug'2011	34.1	0	0	0	0	0	0	0	0	0	0	34.1
Sep'2011	5.93	0	0	0	0	0	0	0	0	0	0	5.93
Oct'2011	1.38	0	0	0	0	0	0	0	0	0	0	1.38
Nov'2011	1.92	0	0	0	0	0	0	0	0	0	0	1.92
Dec'2011												
Jan'2012												
Feb'2012												
Mar'2012												
Apr'2012												
May'2012												
Jun'2012												
Jul'2012												
Aug'2012												
Sep'2012												
Oct'2012												
Nov'2012												
Dec'2012												
Total	43.33	0	0	0	0	0	0	0	0	0	0	43.33

- Notes:
- 1 The performance targets are given in PS clause 25.20A(4)
  - 2 The waste flow table shall also include C & D materials that are specified in the Contract to be imported for use at the Site.
  - 3 Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging material.
  - 4 The summary table shall be submitted to the Engineer's Representative monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.20

**Kai Tak Development - Stage 2 Infrastructure Works at North Apron Area of Kai Tak Airport  
for Residential Development and Government Facilities**

**Monthly Programme for Disposal of C& D Materials**

Month No.	Month	Estimated non-Inert C&D material to be Disposed (t)	Actual C&D material Disposed (t)
1	Jul-11	0	0
2	Aug-11	100	440.08
3	Sep-11	100	31.74
4	Oct-11	100	6.61
5	Nov-11	100	1.89
6	Dec-11	100	
7	Jan-12	100	
8	Feb-12	100	
9	Mar-12	100	
10	Apr-12	100	
11	May-12	100	
12	Jun-12	100	
13	Jul-12	100	
14	Aug-12	100	
15	Sep-12	100	
16	Oct-12	100	
17	Nov-12	100	
18	Dec-12	100	
19	Jan-13	100	
20	Feb-13	100	
21	Mar-13	100	
22	Apr-13	100	
23	May-13	100	
24	Jun-13	100	
25	Jul-13	100	
26	Aug-13	100	
27	Sep-13	100	
28	Oct-13	100	
29	Nov-13	100	
30	Dec-13	100	
31	Jan-14	100	
32	Feb-14	100	
33	Mar-14	100	
34	Apr-14	100	

Note: No inert C&D materials will be disposed off the Site and all non-inert C&D materials will be disposed of at NENT.

**C&D Material Disposal**

