

香港電燈有限公司
The Hongkong Electric Co., Ltd.



**Improvement Dredging for
Lamma Power Station Navigation Channel
Quarterly Environmental Monitoring & Audit Report**

November 2020 – January 2021

香港電燈有限公司
The Hongkong Electric Co., Ltd.



ENVIRONMENTAL IMPACT ASSESSMENT (EIA) ORDINANCE, CAP. 499

ENVIRONMENTAL PERMIT NO. EP-535/2017

**IMPROVEMENT DREDGING FOR
LAMMA POWER STATION NAVIGATION CHANNEL**



Report Title	Quarterly EM&A Summary Report (November 2020 to January 2021)
Date	12 March 2021
Certified by	 (Mr. Kenneth Fung, Environmental Team Leader)
Verified by	 Mr. Y T Tang (AECOM Asia Company Limited, Independent Environmental Checker)

TABLE OF CONTENT

EXECUTIVE SUMMARY

- 1. INTRODUCTION..... 3**
 - 1.1 Background 3
 - 1.2 Project Organisation 3
 - 1.3 Construction Works undertaken during the Reporting Period 3
 - 1.4 Summary of EM&A Requirements 5
- 2. WATER QUALITY MONITORING 9**
- 3. ENVIRONMENTAL AUDIT 10**
 - 3.1 Review of Environmental Monitoring Procedures 10
 - 3.2 Assessment of Environmental Monitoring Results 10
 - 3.3 Site Environmental Audit 11
 - 3.4 Status of Environmental Licensing and Permitting 11
 - 3.5 Implementation Status of Environmental Mitigation Measures 12
 - 3.6 Implementation Status of Alert/Event and Action Plans 12
 - 3.7 Implementation Status of Environmental Complaint Handling Procedures 12
 - 3.8 Environmental Summon and Successful Prosecution 13
- 4. CONCLUSION..... 14**

LIST OF TABLES

Table 1.1	Construction Activities and Their Corresponding Environmental Mitigation Measures
Table 3.1	Summary of Alert, Action and Limit Level Exceedances on Monitoring Parameters
Table 3.2	Estimated Amounts of Waste Generated
Table 3.3	Summary of Environmental Licensing and Permit Status
Table 3.4	Environmental Complaints Received
Table 3.5	Outstanding Environmental Complaints Carried Over

LIST OF FIGURE

Figure 1.1	Project Area
Figure 1.2	Location of Dumping Area (South Cheung Chau Open Sea Sediment Disposal Area)
Figure 1.3	Location of Dumping Area (East of Sha Chau Contaminated Mud Pit)

ANNEX

Annex A	Organisation Chart
Annex B	Amount of Dredged and Dumped Marine Sediment
Annex C	Water Quality Monitoring Results
Annex D	Alert/Event and Action Plans
Annex E	Site Audit Summary
Annex F	Summary of EMIS

EXECUTIVE SUMMARY

The actual dredging work for the “Improvement Dredging for Lamma Power Station Navigation Channel” (the Project) commenced on 18 February 2020. This is the 4th quarterly Environmental Monitoring and Audit (EM&A) Summary report for the Project prepared by the Environmental Team (ET). This report presents the results of impact monitoring for the said project in the period from November 2020 to January 2021.

Marine water quality monitoring was performed. The results were checked against the established Alert, Action and Limit levels. The implementation status of the environmental mitigation measures, Alert/Event and Action Plans and environmental complaint handling procedures were also checked.

Construction Activities Undertaken

The major construction activities during the reporting period were dredging and dumping of dredged mud. Two grab dredgers were deployed and operated within the Project Area. Uncontaminated materials were dumped at the designated location within the South Cheung Chau Open Sea Sediment Disposal Area. The maximum hourly and daily dredging rates actually achieved by the contractors were within the limits specified in the latest dredging schedule.

Environmental Monitoring Works

All monitoring work at designated stations was performed as scheduled in the reporting period.

Water Quality

The water quality monitoring results for Dissolved Oxygen (DO) and Turbidity obtained during the reporting period were within their corresponding Action Levels, Limit Levels and Alert Levels. For Suspended Solid (SS) there were eleven (11) Action Level exceedances and one (1) Limit Level exceedance recorded in the reporting period. All cases were investigated and the investigations concluded that all the cases were not related to the Project.

Site Environmental Audit

Site audits were carried out by ET on a weekly basis to monitor environmental issues at the construction sites to ensure that all mitigation measures were implemented timely and properly. Thirteen site audits were performed in the reporting period.

Independent Environmental Checker (IEC) conducted a site inspection on 27 November 2020, 14 December 2020 and 25 January 2021 to audit the water quality monitoring works/ site works. The site conditions were generally satisfactory. The site audit findings for the reporting period are summarized in [Annex E](#).

Environmental Licensing and Permitting

Description	Permit No.	Valid Period		Issued To	Date of Issuance
		From	To		
Environmental Permit	EP-535/2017	10/10/2017	-	HK Electric	10/10/2017
Construction Noise Permit	GW-RS0486-20	07/08/2020	06/02/2021	Contractor	17/07/2020
Marine Dumping Permit	EP/MD/21-060	16/10/2020	31/01/2021	Contractor	15/10/2020
Marine Dumping Permit	EP/MD/21-061	16/10/2020	31/01/2021	Contractor	15/10/2020

Implementation Status of Environmental Mitigation Measures

Environmental mitigation measures for the construction activities as recommended in the EM&A manual were implemented in the reporting period.

Environmental Complaints

No complaint against the Project was received in the reporting period.

Environmental Summon and Successful Prosecution

No notifications of summon or successful prosecution was received in the reporting period.

Concluding Remarks

The environmental performance of the project during the reporting period was generally satisfactory.

1. INTRODUCTION

1.1 Background

The Environmental Team (hereinafter called the “ET”) was formed within the Hongkong Electric Co. Ltd (HK Electric) to undertake Environmental Monitoring and Audit for “Improvement Dredging for Lamma Power Station Navigation Channel” (hereinafter called the “Project”). Under the requirements of Section 3 of Environmental Permit EP-535/2017, an EM&A programme for impact environmental monitoring is required to be implemented. In accordance with the EM&A Manual, environmental monitoring of water quality and regular environmental audits are required for the Project.

The Project involves re-profiling the Lamma Power Station Navigation Channel (the “Channel”) to a target depth of -16.5 mPD with an estimated sediment quantity up to approx. 3.2 million m³, subject to fine-tuning against the actual existing seabed profile. The Project Area is shown in [Figure 1.1](#).

The majority of dredging work is to be carried out by Trailer Suction Hopper Dredger (TSHD) whereas the minority of dredging work for remedial trimming and near the existing jetty structure is to be carried out by grab dredger. The construction works of the Project was commenced in February 2020.

This report summarizes the environmental monitoring and audit work for the Project for the period from November 2020 to January 2021.

1.2 Project Organisation

The management structure to oversee the Project includes the following:

- Project Proponent (HK Electric);
- Environmental Protection Department (EPD);
- Engineer or Engineer’s Representative (ER);
- Independent Environmental Checker (IEC);
- Environmental Team (ET); and
- Contractor.

The project organisation chart and environmental team organisation chart for the construction EM&A programme are shown in [Annex A](#).

1.3 Construction Works undertaken during the Reporting Period

Construction activities undertaken during the reporting report for this Project were dredging and dumping of dredged mud. Grab dredger was deployed and operated within the Project Area. The total volume of dredged materials from 1 November 2020 to 31 January 2021 was 101,400 m³. Uncontaminated materials were dumped at the designated location within the South Cheung Chau Open Sea Sediment Disposal Area and the total dumped volume in reporting period was 101,400 m³. The location of dumping site is shown in [Figure 1.2](#) and [Figure 1.3](#).

Daily records of dredged / dumped volume are presented in [Annex B](#). The maximum hourly and daily dredging rates achieved by the contractors were within the limits specified in the latest dredging schedule.

The main construction activities carried out during the reporting period and the corresponding environmental mitigation measures are summarized in [Table 1.1](#). The implementation of major mitigation measures in the period is provided in [Annex F](#).

Table 1.1 Construction Activities and Their Corresponding Environmental Mitigation Measures

Construction Activities	Environmental Mitigation Measures
Dredging	<p>Water Quality</p> <ul style="list-style-type: none"> – There was no concurrent or mixed use of grab dredger and TSHD operation. – Closed grab capacity was not less than 8m³ (except for dredging works near submarine pipeline). – Cage-type silt curtain (at least 10m depth) was used for grab dredger operation. – No operation of more than 5 grab dredgers concurrently at any time was allowed. – Both maximum total hourly and daily dredging rates as specified in the latest dredging schedule were strictly followed. – Vessel speeds within the Project Area were reduced to maximum speed limit. – Neither overflow nor using of lean mixture overboard (LMOB) system was occurred. – All barges for transportation of dredged materials were fitted with tight bottom seals to prevent leakage. <p>Marine Ecology</p> <ul style="list-style-type: none"> – No dredging on Zone 4 of the navigation channel during the calving season for the Finless Porpoise. – All construction related vessels travelled to and from the Project Area followed the designated route to avoid the Finless Porpoise habitat area. – The dumping of chemicals, rubbish, oils etc. into the water was strictly prohibited. <p>Hazard to Life</p> <ul style="list-style-type: none"> – Marine vessels should avoid traveling during berthing and unberthing of coal vessel. – As far as practicable, marine vessels should avoid traveling after sunset or under low visibility when the works area is near submarine pipeline. – Working vessel not to stay right above the submarine pipeline unless it is necessary. <p>Noise</p> <ul style="list-style-type: none"> – General noise mitigation measures were employed at work site throughout the construction phase. – The number and type of plants and operation conditions as

Construction Activities	Environmental Mitigation Measures
	<p style="text-align: center;">specified in the CNP were strictly followed.</p> <p>Waste Management</p> <ul style="list-style-type: none">– All barges for transportation of dredged materials were fitted with tight bottom seals to prevent leakage.– All vessels were filled to a level such that dredged materials would not spill over during loading and transportation.– Dredged wastes were disposed of at Licensed dumping site.– Records of the quantities of waste generated and disposed of off-site were taken.

1.4 Summary of EM&A Requirements

The EM&A program requires environmental monitoring of water quality. The detailed EM&A monitoring work for water quality is described in [Sections 2](#) of this report.

The following environmental audits are summarized in [Section 3](#) of the report:

- Environmental monitoring results;
- Waste Management Records;
- Weekly site audit results;
- The status of environmental licensing and permits for the Project;
- The implementation status of environmental protection and pollution control/ mitigation measures.

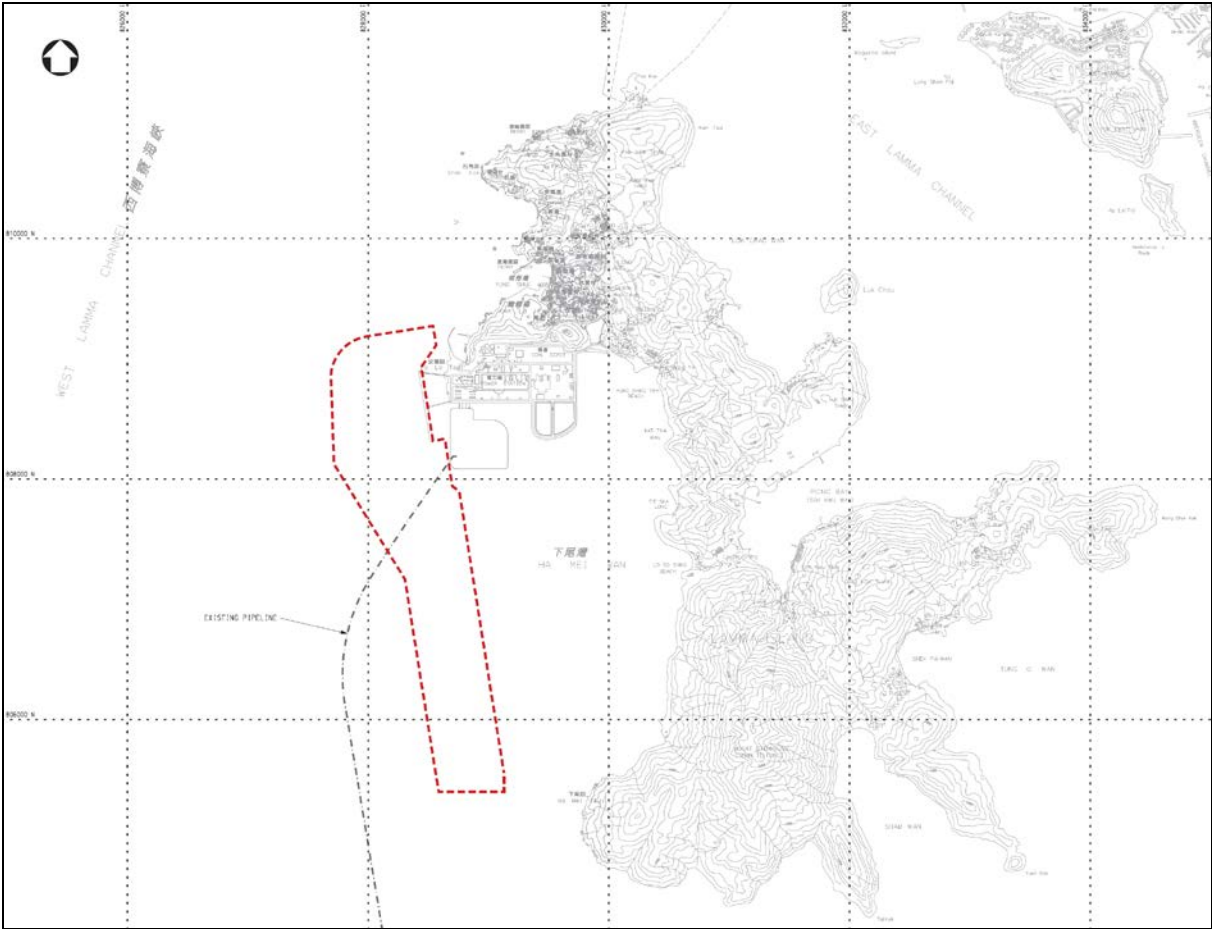


Figure 1.1 Project Area

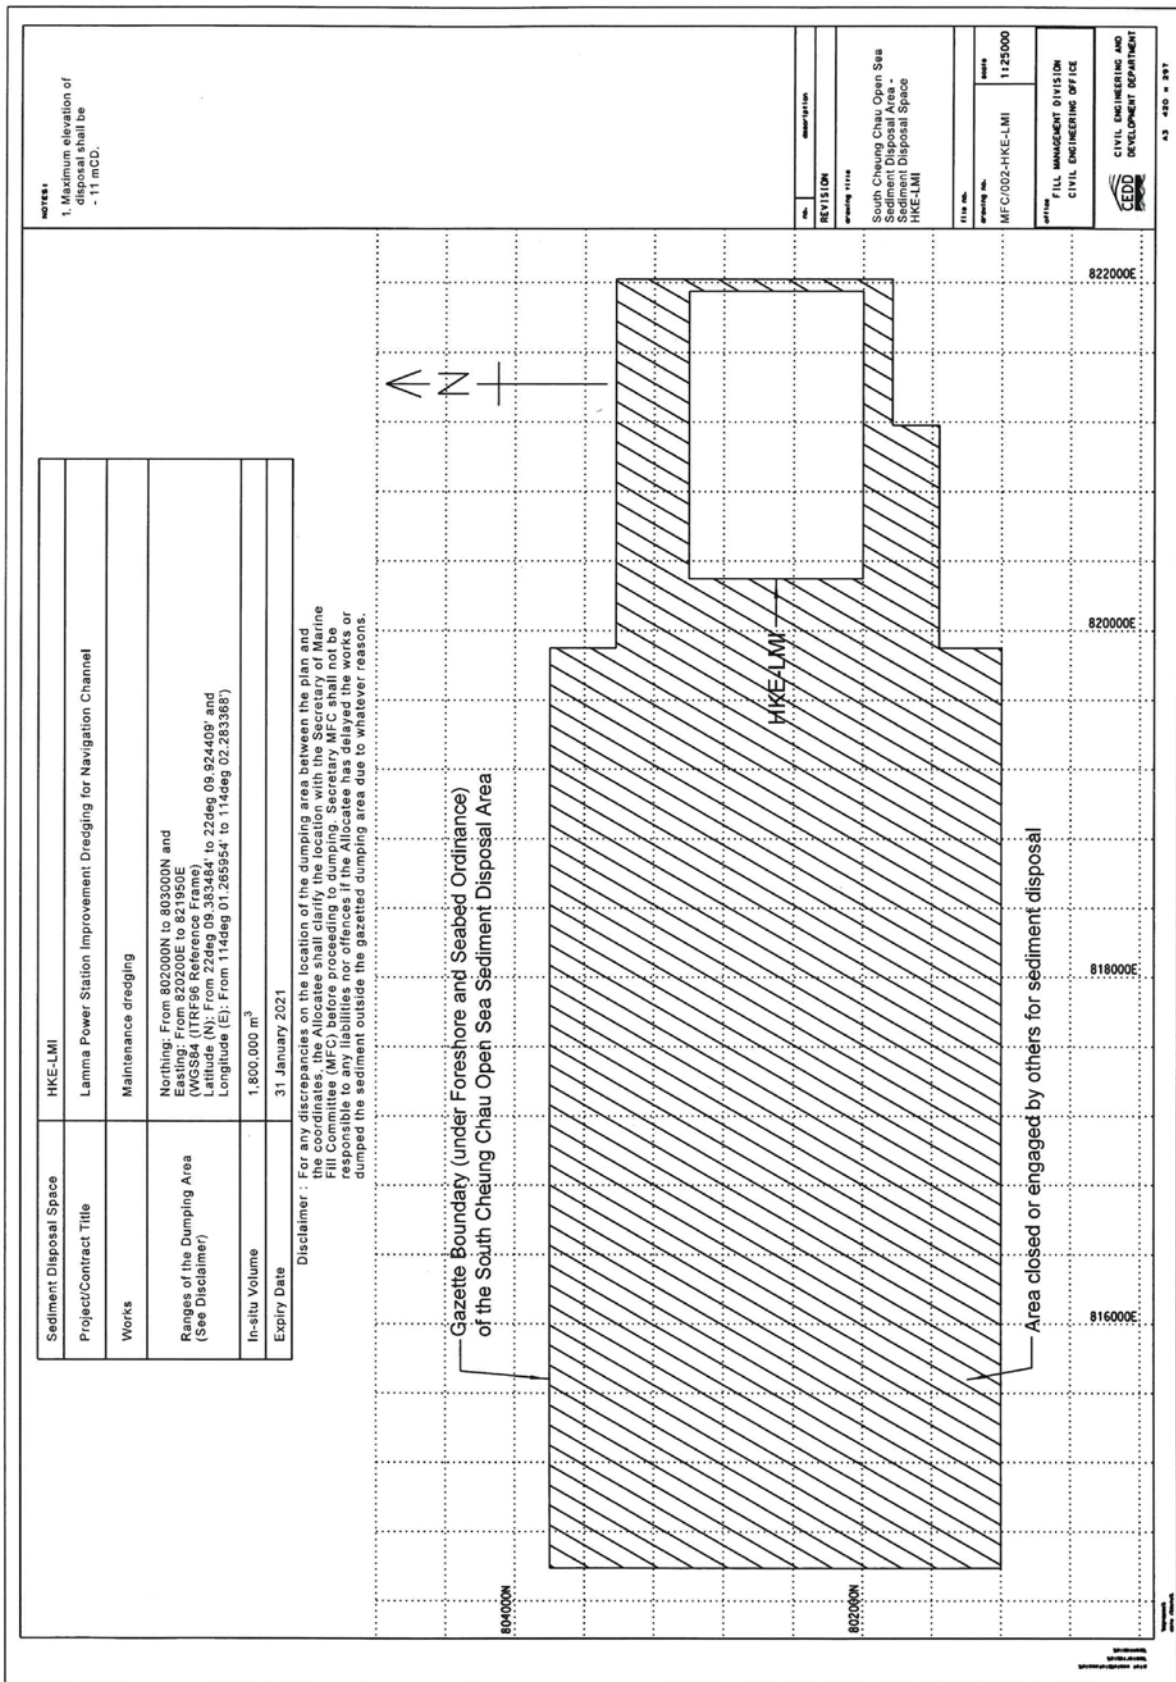


Figure 1.2 Location of Dumping Site (South Cheung Chau Open Sea Sediment Disposal Area)

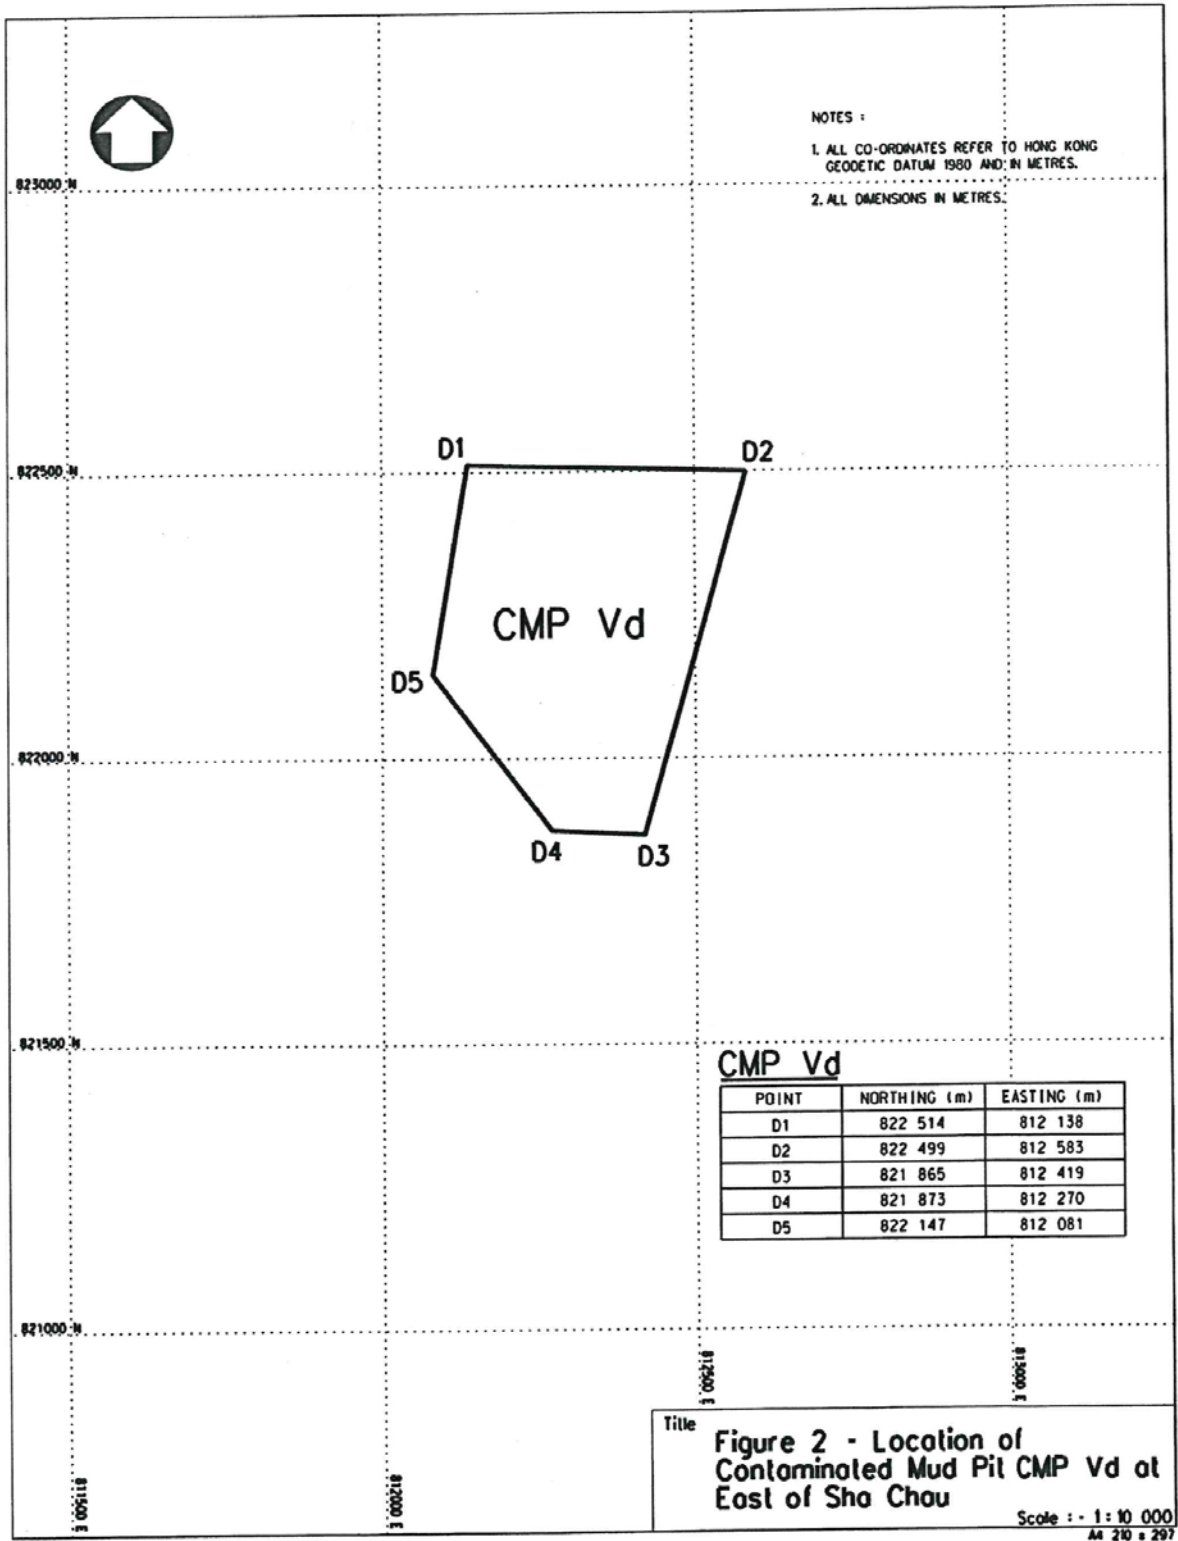


Figure 1.3 Location of Dumping Site (East of Sha Chau Contaminated Mud Pit)

2. WATER QUALITY MONITORING

Marine water quality monitoring was carried out during the marine works to detect and check for any deterioration in water quality and ensure that timely action is taken to rectify deteriorations that are due to the Project.

HK Electric commissioned Mott MacDonald Hong Kong Limited to carry out water quality monitoring works of the Project. Details of the water quality monitoring results and the associated alert/event and action plans presented in the Quarterly Water Quality Monitoring Report are shown in [Annex C](#).

3. ENVIRONMENTAL AUDIT

3.1 Review of Environmental Monitoring Procedures

The environmental monitoring procedures were regularly reviewed by the Environmental Team. No modification to the existing monitoring procedures was recommended.

3.2 Assessment of Environmental Monitoring Results

Monitoring results for Water Quality

Table 3.1 Summary of Alert, Action and Limit Level Exceedances on Monitoring Parameters

Item	Parameter Monitored	Monitoring Period	No. of Exceedances			Alert/Event and Action Plans Implementation Status and Results
			Alert Level	Action Level	Limit Level	
Water						
1	DO (Surface & Middle)	01/11/2020 31/01/2021	0	0	0	Investigation concluded that the exceedance was not related to the Project. Please refer to Section 2 and Annex C of the report for details.
2	DO (Bottom)	01/11/2020 31/01/2021	0	0	0	
3	Turbidity	01/11/2020 31/01/2021	0	0	0	
4	SS	01/11/2020 31/01/2021	N.A.	11	1	

There were eleven (11) Action Level exceedances and one (1) Limit Level exceedance of Suspended Solid (SS) recorded in the reporting period. These exceedances were investigated and found that the affected SR stations were either upstream of the Project during the corresponding tide, or located at a great distance from the Project site, or the exceedances appeared to be due to local factors not related to the Project, or no dredging work was carried out on the dates of exceedance. No further action was required. Nevertheless IEC, Engineer and the construction contractor had been informed of the exceedances accordingly as per requirements of the EM&A Manual. For details, please refer to [Section 2](#) and [Annex C](#) of the report.

Waste Management

The estimated amounts of waste generated in reporting period are shown in [Table 3.2](#).

Table 3.2 Estimated Amounts of Waste Generated

Period	Waste Type	Estimated Amount (m ³)
November 2020	Dredged Materials – Marine Mud	85,200
December 2020	Dredged Materials – Marine Mud	16,200
January 2021	Dredged Materials – Marine Mud	0

The total bulk volume of dredged material was 101,400 m³.

3.3 Site Environmental Audit

Site audits were carried out by ET on a weekly basis to monitor environmental issues at the construction sites to ensure that all mitigation measures were implemented timely and properly. Four site audits were performed in the reporting period.

Independent Environmental Checker (IEC) conducted a site inspection on 27 November 2020, 14 December 2020 and 25 January 2021 to audit the water quality monitoring and/or site works. The site conditions were generally satisfactory. The site audit findings for the reporting period are summarized in [Annex E](#).

3.4 Status of Environmental Licensing and Permitting

All permits/licenses obtained for the project are summarised in [Table 3.3](#).

Table 3.3 Summary of Environmental Licensing and Permit Status

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Environmental Permit	EP-535/2017	10/10/2017	-	The whole construction work site	Valid
Construction Noise Permit	GW-RS0486-20	07/08/2020	06/02/2021	Operation of PME during the restricted hours (00:00-24:00 hours on general holidays, and 00:00-07:00 and 19:00-2400 hours on any day not being a general holiday)	Valid
Marine Dumping Permit	EP/MD/21-060	16/10/2020	31/01/2021	Dumping at East of Sha Chau Contaminated Mud Pit	Valid

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Marine Dumping Permit	EP/MD/21-061	16/10/2020	31/01/2021	Dumping at South Cheung Chau Open Sea Sediment Disposal Area	Valid

3.5 Implementation Status of Environmental Mitigation Measures

Mitigation measures detailed in the permits and the EM&A Manual are required to be implemented. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in [Annex F](#).

3.6 Implementation Status of Alert/Event and Action Plans

According to the findings presented in water quality monitoring results obtained during the reporting period, some of the testing results triggered the relevant Action and Limit Levels, and investigations were conducted accordingly. The investigations concluded that all cases were not related to the Project; hence, the Project did not induce adverse impact to all water quality sensitive receivers. All required actions under the Event and Action Plan were followed.

The Alert/Event and Action Plans for water quality extracted from the EM&A Manual are presented in [Annex D](#).

3.7 Implementation Status of Environmental Complaint Handling Procedures

During the reporting period, there was no environmental complaint against the Project was received.

Table 3.4 Environmental Complaints Received

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

Table 3.5 Outstanding Environmental Complaints Carried Over

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

3.8 Environmental Summon and Successful Prosecution

No notifications of summon or successful prosecution was received in the reporting period.

4. CONCLUSION


Environmental monitoring was performed as required in the reporting period. The water quality monitoring results for DO and turbidity obtained during the reporting period were within the corresponding Action, Limit or Alert Levels stipulated in the EM&A programme. For SS, some of the testing results triggered the relevant Action or Limit Levels, and investigations were conducted accordingly. The investigations concluded that the cases were not related to the Project.

Environmental mitigation measures recommended in the EM&A manual for the Project were implemented in the reporting period. No complaint against the Project was received. No prosecution and summons was received for this Project in the reporting period.

The environmental performance of the Project was generally satisfactory.

Annex A Organization Chart

A1: Project Organisation Chart

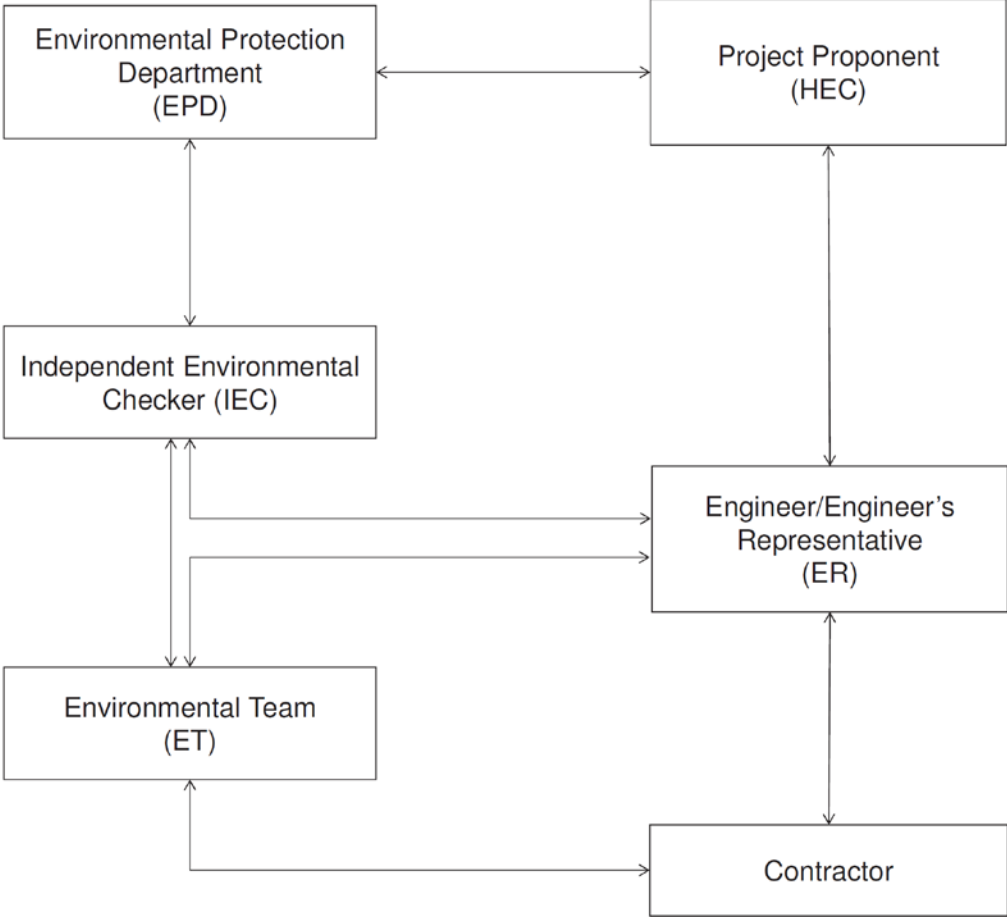


A2: Environmental Team Organisation Chart



Improvement Dredging for Lamma Power Station Navigation Channel (EP-535/2017)

Environmental Team Organization Chart

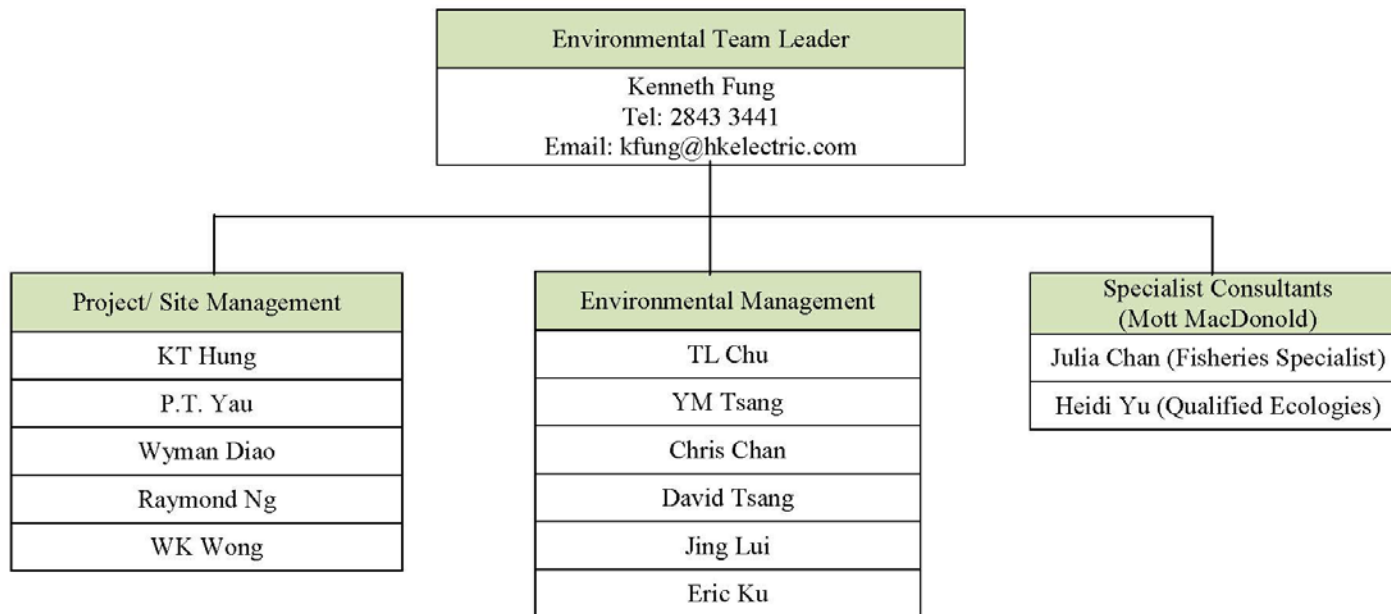

Annex B Amount of Dredged and Dumped Marine Sediment

Date	Dredging Time	Dredged Marine Mud (bulk volume m ³)	Dumping Time	Dumped Marine Mud (bulk volume m ³)
01/11/2020	00:00 – 23:59	3,600	00:00 – 23:59	4,200
02/11/2020	00:00 – 23:59	4,800	00:00 – 23:59	4,200
03/11/2020	00:00 – 23:59	4,800	00:00 – 23:59	4,800
04/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	4,800
05/11/2020	00:00 – 23:59	600	00:00 – 23:59	1,200
06/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	2,400
07/11/2020	00:00 – 23:59	2,400	00:00 – 23:59	2,400
08/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	3,000
09/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	3,000
10/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	4,800
11/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	4,200
12/11/2020	00:00 – 23:59	3,600	00:00 – 23:59	3,600
13/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	2,400
14/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	3,600
15/11/2020	00:00 – 23:59	0	00:00 – 23:59	1,200
16/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	3,000
17/11/2020	00:00 – 23:59	1,200	00:00 – 23:59	0
18/11/2020	00:00 – 23:59	4,800	00:00 – 23:59	4,800
19/11/2020	00:00 – 23:59	3,600	00:00 – 23:59	3,600
20/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	4,800
21/11/2020	00:00 – 23:59	0	00:00 – 23:59	600
22/11/2020	00:00 – 23:59	2,400	00:00 – 23:59	1,800
23/11/2020	00:00 – 23:59	0	00:00 – 23:59	600
24/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	3,000
25/11/2020	00:00 – 23:59	3,000	00:00 – 23:59	2,400
26/11/2020	00:00 – 23:59	4,200	00:00 – 23:59	3,600
27/11/2020	00:00 – 23:59	600	00:00 – 23:59	1,200
28/11/2020	00:00 – 23:59	1,800	00:00 – 23:59	2,400
29/11/2020	00:00 – 23:59	2,400	00:00 – 23:59	1,200
30/11/2020	00:00 – 23:59	2,400	00:00 – 23:59	2,400
Total in the Month		85,200		85,200
Accumulated Total		4,484,100		4,484,100

Date	Dredging Time	Dredged Marine Mud (bulk volume m ³)	Dumping Time	Dumped Marine Mud (bulk volume m ³)
01/12/2020	00:00 – 23:59	1,200	00:00 – 23:59	1,200
02/12/2020	-	-	-	-
03/12/2020	00:00 – 23:59	600	00:00 – 23:59	0
04/12/2020	00:00 – 23:59	1,800	00:00 – 23:59	1,800
05/12/2020	00:00 – 23:59	600	00:00 – 23:59	600
06/12/2020	00:00 – 23:59	2,400	00:00 – 23:59	2,400
07/12/2020	00:00 – 23:59	2,400	00:00 – 23:59	2,400
08/12/2020	00:00 – 23:59	0	00:00 – 23:59	600
09/12/2020	-	-	-	-
10/12/2020	-	-	-	-
11/12/2020	00:00 – 23:59	600	00:00 – 23:59	600
12/12/2020	00:00 – 23:59	1,800	00:00 – 23:59	1,800
13/12/2020	00:00 – 23:59	2,400	00:00 – 23:59	2,400
14/12/2020	00:00 – 23:59	1,800	00:00 – 23:59	1,800
15/12/2020	00:00 – 23:59	600	00:00 – 23:59	600
16/12/2020	-	-	-	-
17/12/2020	-	-	-	-
18/12/2020	-	-	-	-
19/12/2020	-	-	-	-
20/12/2020	-	-	-	-
21/12/2020	-	-	-	-
22/12/2020	-	-	-	-
23/12/2020	-	-	-	-
24/12/2020	-	-	-	-
25/12/2020	-	-	-	-
26/12/2020	-	-	-	-
27/12/2020	-	-	-	-
28/12/2020	-	-	-	-
29/12/2020	-	-	-	-
30/12/2020	-	-	-	-
31/12/2020	-	-	-	-
Total in the Month		16,200		16,200
Accumulated Total		4,500,300		4,500,300

Date	Dredging Time	Dredged Marine Mud (bulk volume m ³)	Dumping Time	Dumped Marine Mud (bulk volume m ³)
01/01/2021	-	-	-	-
02/01/2021	-	-	-	-
03/01/2021	-	-	-	-
04/01/2021	-	-	-	-
05/01/2021	-	-	-	-
06/01/2021	-	-	-	-
07/01/2021	-	-	-	-
08/01/2021	-	-	-	-
09/01/2021	-	-	-	-
10/01/2021	-	-	-	-
11/01/2021	-	-	-	-
12/01/2021	-	-	-	-
13/01/2021	-	-	-	-
14/01/2021	-	-	-	-
15/01/2021	-	-	-	-
16/01/2021	-	-	-	-
17/01/2021	-	-	-	-
18/01/2021	-	-	-	-
19/01/2021	-	-	-	-
20/01/2021	-	-	-	-
21/01/2021	-	-	-	-
22/01/2021	-	-	-	-
23/01/2021	-	-	-	-
24/01/2021	-	-	-	-
25/01/2021	-	-	-	-
26/01/2021	-	-	-	-
27/01/2021	-	-	-	-
28/01/2021	-	-	-	-
29/01/2021	-	-	-	-
30/01/2021	-	-	-	-
31/01/2021	-	-	-	-
Total in the Month		0		0
Accumulated Total		4,500,300		4,500,300

Note:-

As the bulking factor (i.e. bulking factor of 4 for TSHD & 1.3 for Hopper Barge in accordance with assumptions in the approved dumping permit by EPD) of dredged marine mud is found varying considerably at different locations in the navigation channel depending on the depth of high spots to be removed, the final in-situ as-dredged volume will be determined by swath surveys of the navigation channel before and after the dredging work.

Following the interim survey carried out from 13 to 16 March 2020, the bulking factor for TSHD has been adjusted from 4 to 2.8 as directed by EPD. Subsequent planning and control of dredging rates for coming works would be based on the adjusted bulking factor.

Annex C

Water Quality Monitoring Results



Improvement Dredging for Lamma Power Station Navigation Channel

Construction Phase Quarterly Water Quality
Monitoring Report No. 4 (November 2020–
January 2021)

February 2021

Mott MacDonald
3/F International Trade
Tower
348 Kwun Tong Road
Kwun Tong
Kowloon
Hong Kong

T +852 2828 5757
mottmac.hk

The Hongkong Electric
Company Limited

Improvement Dredging for Lamma Power Station Navigation Channel

Construction Phase Quarterly Water Quality
Monitoring Report No. 4 (November 2020–
January 2021)

February 2021

Contents

Executive summary	1
1 Introduction	2
2 Monitoring Methodology	3
2.1 Monitoring Frequency and Locations	3
2.2 Monitoring Parameters	4
3 Water Quality Performance Limits	5
3.1 Action and Limit Levels	5
3.2 Alert Levels	6
3.3 Review of Alert Levels	6
4 Monitoring Results	7
5 Conclusion	8
Appendix	9
A. Graphical Presentations of Water Quality Monitoring Results	10
Tables	
Table 2.1: Locations of Water Quality Monitoring Stations	3
Table 3.1: Calculated Action and Limit Levels	5
Table 3.2: Calculated Initial Alert Levels	6
Table 4.1: Summary of SS Exceedances	7

Figures

Figure 2.1: Water Quality Monitoring Locations

Executive summary

The Project “Improvement Dredging for Lamma Power Station Navigation Channel” commenced on 18 February 2020. This is the fourth quarterly Water Quality Monitoring report for the Project. This report presents the results of impact monitoring on marine water quality for the Project from November 2020 to January 2021.

During this reporting period, a total of 39 days of marine water quality monitoring was carried out. The water quality monitoring results for dissolved oxygen (DO) and turbidity obtained during the reporting period were within the corresponding Action and Limit Levels for sensitive receiver stations and within the Alert Levels for near stations as stipulated in the EM&A programme. For suspended solids (SS), some of the results triggered the relevant Action or Limit Levels, and the corresponding investigations concluded that the cases were not related to the Project. To conclude, the dredging activities in the reporting period did not cause adverse impact to all water quality sensitive receivers.

1 Introduction

On 10 October 2017, the Environment Impact Assessment (EIA) Report (Register No.: AEIAR-212/2017) for the “Improvement Dredging for Lamma Power Station Navigation Channel” (the Project) was approved and an Environmental Permit (EP) (No. EP-535/2017) was issued for the construction and operation of the Project. Mott MacDonald Hong Kong Limited was commissioned by The Hongkong Electric Company, Limited to carry out the water quality monitoring works of the Project during the construction phase.

The purpose of the Project is to provide and maintain safe clearance for ocean-going marine vessels delivering coal to Lamma Power Station (LPS) via the Lamma Power Station Navigation Channel (the “Channel”), through the dredging of naturally accumulating sediment from the seabed. In order to meet the requirements for continued safe passage, the construction phase of the Project involves improvement dredging of the Channel to a target dredge depth¹ of -16.5 mPD.

The construction phase of the Project commenced on 18 February 2020. This Water Quality Monitoring Report summarizes the water quality monitoring as part of the EM&A programme for the Project for the months of November and December 2020 and January 2021.

¹ While the Project aims to dredge to a target depth of -16.5 mPD, some overdredge may occur due to the limited precision control of dredging depths in practice.

2 Monitoring Methodology

2.1 Monitoring Frequency and Locations

The water quality monitoring was conducted three days per week during the reporting period at mid-flood and mid-ebb tides. The monitoring was conducted at a total of 16 water quality monitoring stations, comprising eight SR stations, five near stations and three control stations. Details of the monitoring locations are shown in **Figure 2.1** and **Table 2.2**. It should be noted that the location of SR8 provided in **Table 2.2** is approximate due to changing location of fish rafts under different tidal and wind condition. Water quality monitoring at SR8 was conducted at the nearest safely accessible location to the Fish Culture Zone. Moreover, as specified in the Updated EM&A Manual, SR2 and SR3 should be monitored during March and October only. Therefore, SR2 and SR3 are not monitored in this reporting period.

Table 2.1: Locations of Water Quality Monitoring Stations

ID	Station	Easting	Northing	Remarks
SR1	HK Electric Power Station Intake	829194	808600	Monitored for SS only
SR2	Hung Shing Yeh Beach	830200	808700	Monitored during bathing season only (March to October inclusive)
SR3	Lo So Shing Beach	830450	807300	Monitored during bathing season only (March to October inclusive)
SR4	Marine Ecological Habitat at Pak Kok	829600	811630	
SR5	Marine Ecological Habitat at Shek Kok Tsui	828560	811100	
SR6	Marine Ecological Habitat at Ha Mei Wan	829760	805520	
SR7	Marine Ecological Habitat at Southwest of Lamma	829590	804520	
SR8	Fish Culture Zone at Lo Tik Wan	831265	809115	
SR9	Fish Culture Zone at Sok Kwu Wan	831600	807765	
SR10	Fish Culture Zone at Cheung Sha Wan	819160	810780	
A1	Near station for Zone 1	828543	809573	For monitoring potential impacts to SR5 and SR4 during flood tide
A2	Near station for Zone 2	829053	807945	For monitoring potential impacts to SR1 and SR2 during flood tide
A3	Near station for Zone 3	829187	807100	For monitoring potential impacts to SR3 during both flood and ebb tide
A4	Near station for Zone 4 (east)	829427	805520	For monitoring potential impacts to SR6 during ebb tide
A5	Near station for Zone 4 (south)	829267	805134	For monitoring potential impacts to SR7 during ebb tide
C1	Control Station 1	828000	813500	
C2	Control Station 2	825000	808000	

ID	Station	Easting	Northing	Remarks
C3	Control Station 3	829000	802000	

2.2 Monitoring Parameters

For the eight SR stations (SR1 and SR4 to SR10) and three control stations (C1 to C3), monitoring of DO, DO%, pH, temperature, turbidity, salinity, water depth and SS were undertaken. For monitoring of the five near stations (A1 to A5), only the in-situ parameters (DO, DO%, pH, temperature, turbidity, salinity and water depth) were recorded. Other relevant data were also recorded, including monitoring location, time, tidal stage, weather condition and sea condition.

3 Water Quality Performance Limits

3.1 Action and Limit Levels

The Action and Limit levels are summarized in **Table 3.1**.

Table 3.1: Calculated Action and Limit Levels

Parameters	Action Level		Limit Level	
SR1				
SS in mg/L	90		100	
SR2 to SR7				
DO in mg/L	Wet	Dry	Wet	Dry
Surface & Middle	3.1	5.6	2.6	4
Bottom	2.4	5.8	1.9	2
SS in mg/L	9.5 OR 120% of upstream control station(s) at the same tide of the same day, whichever is higher		12.3 OR 130% of upstream control station(s) at the same tide of the same day, whichever is higher	
Turbidity in NTU	9.7 OR 120% of upstream control station(s) at the same tide of the same day, whichever is higher		11.8 OR 130% of upstream control station(s) at the same tide of the same day, whichever is higher	
SR8 to SR10				
DO in mg/L	Wet	Dry	Wet	Dry
Surface & Middle	5	5.6	5	5
Bottom	2.4	5.8	2	2
SS in mg/L	9.5 OR 120% of upstream control station(s) at the same tide of the same day, whichever is higher		12.3 OR 130% of upstream control station(s) at the same tide of the same day, whichever is higher	
Turbidity in NTU	9.7 OR 120% of upstream control station(s) at the same tide of the same day, whichever is higher		11.8 OR 130% of upstream control station(s) at the same tide of the same day, whichever is higher	

Notes:

1. Wet season: April to September; Dry season: October to March.
2. For DO measurement, non-compliance occurs when the monitoring result is lower than the limits.
3. For parameters other than DO, non-compliance of water quality occurs when the monitoring result is higher than the limits.
4. Depth-averaged results are used unless specified otherwise.
5. SR1 is monitored for SS only.
6. All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered as necessary.

3.2 Alert Levels

The Alert levels for water quality at near stations are presented in **Table 4.1**.

Table 3.2: Calculated Initial Alert Levels

Alert Level	A1	A2	A3	A4	A5
Turbidity (NTU)	30.1	18.4	38.8	32.0	24.3
DO (mg/L) – Depth-average, Dry Season	4	4	4	4	4
	OR 0.1 mg/L less than the same day control, whichever is lower				
DO (mg/L) – Bottom, Dry Season	2	2	2	2	2
	OR 0.1 mg/L less than the same day control, whichever is lower				
DO (mg/L) – Depth-average, Wet Season	3	3	3	3	3
	OR 0.1 mg/L less than the same day control, whichever is lower				
DO (mg/L) – Bottom, Wet Season	0.9	0.9	0.9	0.9	0.9
	OR 0.1 mg/L less than the same day control, whichever is lower				

Note: Wet season: April to September; Dry season: October to March.

3.3 Review of Alert Levels

As stated in the Construction Phase Quarterly Water Quality Monitoring Report No. 3 (August–October 2020), it is recommended to review the Alert Levels for turbidity once there is adequate exceedance cases for reference. Since there were no exceedances of turbidity during the reporting period, the existing Alert Levels shown in **Table 3.2** will continue to apply.

4 Monitoring Results

Marine water quality monitoring was conducted as scheduled during the reporting period. Graphical presentations of the monitoring results are provided in **Appendix A**.

The water quality monitoring results for DO and turbidity obtained during the reporting period were within their corresponding Action Levels, Limit Levels and Alert Levels.

For SS, some of the testing results at SR stations triggered the corresponding Action or Limit Levels. The IEC, Engineer and the construction contractor were informed of the exceedances and the Event and Action Plan of the Updated EM&A Manual was initiated. **Table 5.1** presents the summary of the SS exceedances at SR stations during mid-ebb and mid-flood tide for the reporting period.

Table 4.1: Summary of SS Exceedances

Date	Parameter(s)	Affected Station(s)	Tide	Exceedance Type
11 Nov	SS	SR4, SR7, SR9	Flood tide	Action Level
16 Dec	SS	SR10	Ebb tide	Action Level
		SR5, SR6, SR7, SR10	Flood tide	Action Level
		SR8	Flood tide	Limit Level
21 Dec	SS	SR4, SR5, SR10	Ebb tide	Action Level

The investigation findings are summarised below:


- 11 November 2020 – the contractor confirmed that no abnormal operation and spillage occurred and all required mitigation measures were implemented. The investigations found that the affected SR stations were upstream of the Project during the corresponding tide, or located at a great distance from the Project Site with no evidence of effect from the Project, or the exceedance appeared to be due to local factors not related to the Project.
- 16 and 21 December 2020 – no dredging work was carried out during this period hence the causes are not related to the Project.

As all investigations concluded that the cases were not related to the Project, no further action was required.

5 Conclusion

Monitoring work for water quality was conducted during the reporting period in accordance with the updated EM&A Manual.

The water quality monitoring results for DO and turbidity obtained during the reporting period were within the corresponding Action, Limit or Alert Levels stipulated in the EM&A programme. For SS, some of the results triggered the relevant Action or Limit Levels, and investigations were conducted accordingly. The investigations concluded that the cases were not related to the Project. To conclude, the construction activities in the reporting period did not cause adverse impact to all water quality sensitive receivers.

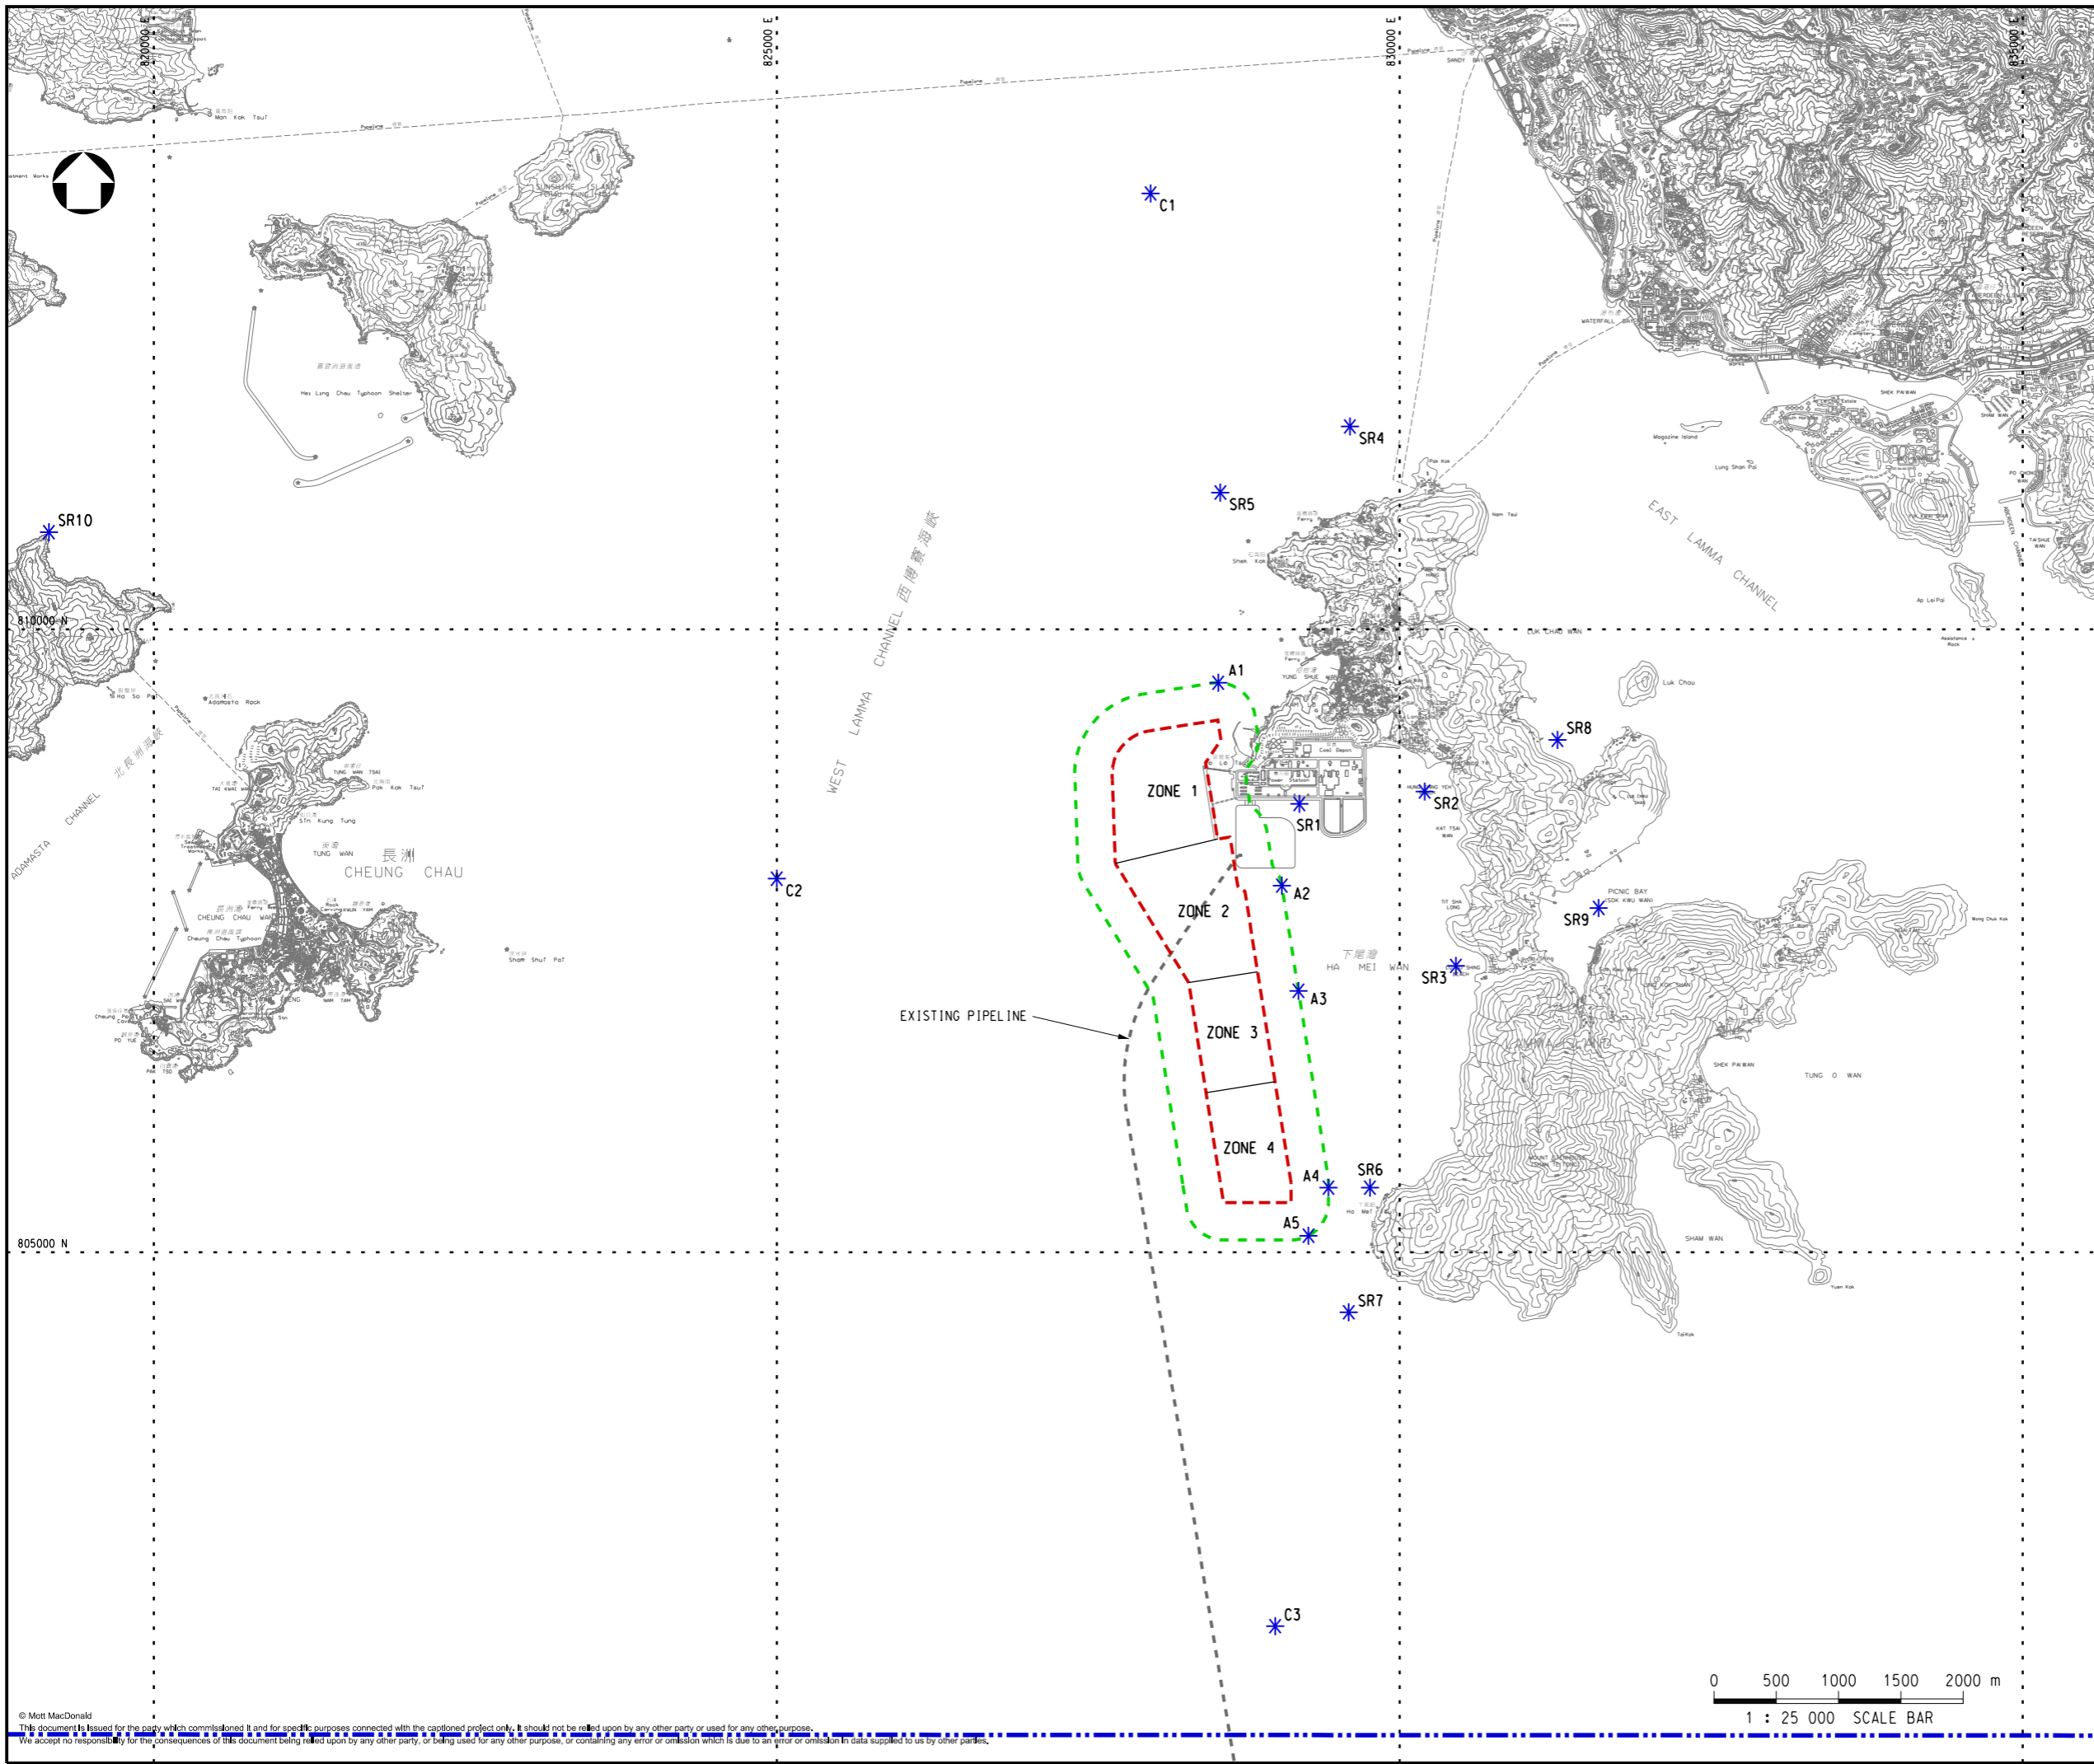

Notes

Key to symbols

- HKSAR BOUNDARY
- PROJECT BOUNDARY
- 300m BUFFER
- * WATER QUALITY MONITORING LOCATION

Reference drawings

P1	JUN 18	MING	FIRST ISSUE	DC	EC
Rev	Date	Drawn	Description	Ch'k'd	App'd

**MOTT
MACDONALD**

20/F AIA Kowloon Tower
Landmark East
100 How Ming Street
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

**港燈
HK Electric**


Project

**IMPROVEMENT DREDGING FOR
LAMMA POWER STATION
NAVIGATION CHANNEL**

Title

**WATER QUALITY MONITORING
LOCATIONS**




Designed	DC	Eng check	DC
Drawn	MING	Coordination	DC
Dwg check	DC	Approved	EC
Scale at A1	Status	Rev	
1:25000	PRE	P1	
Drawing Number		FIGURE 2.1	






Appendix

A.	Graphical Presentations of Water Quality Monitoring Results	10
----	---	----



A. Graphical Presentations of Water Quality Monitoring Results

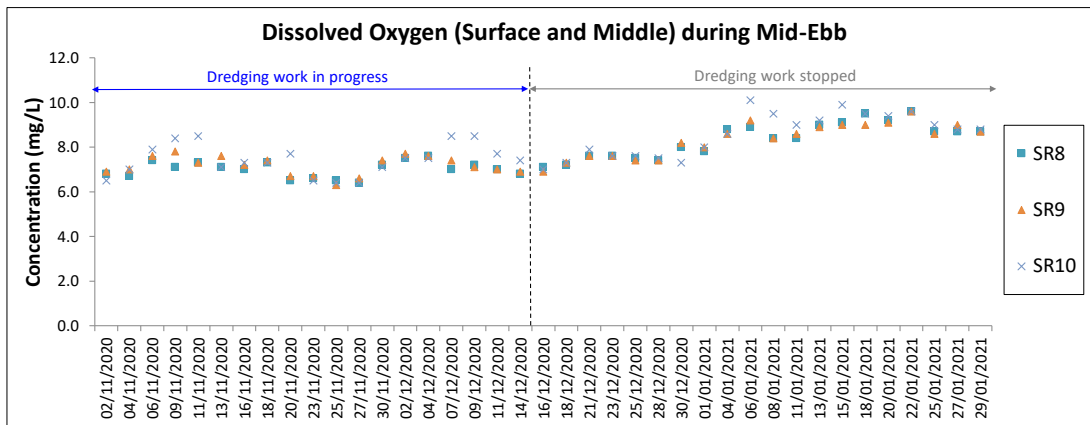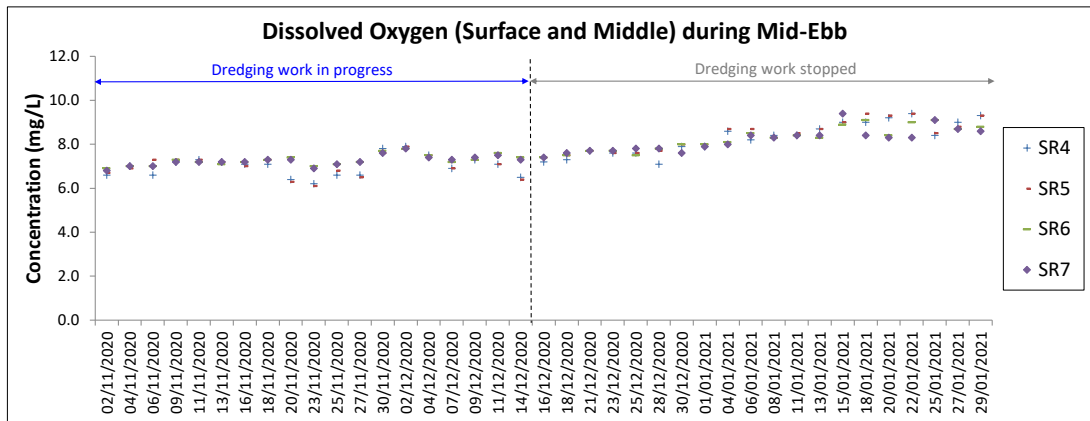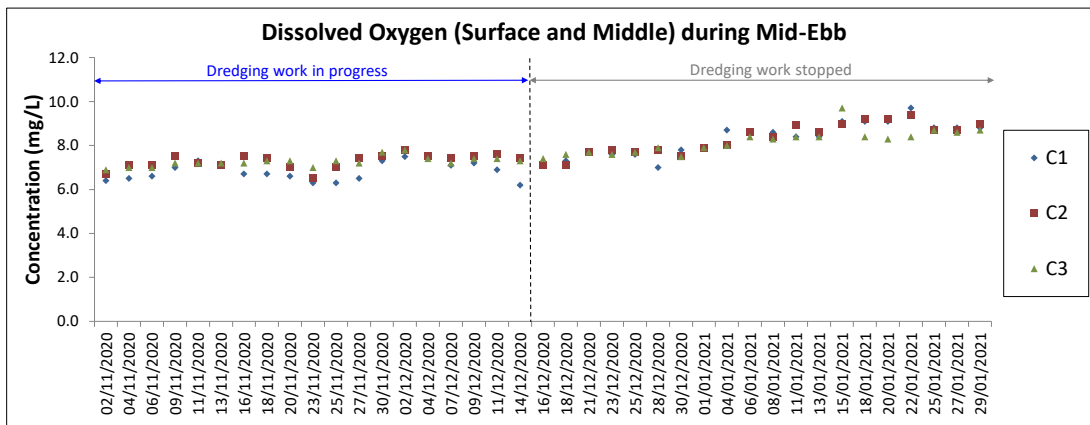





Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

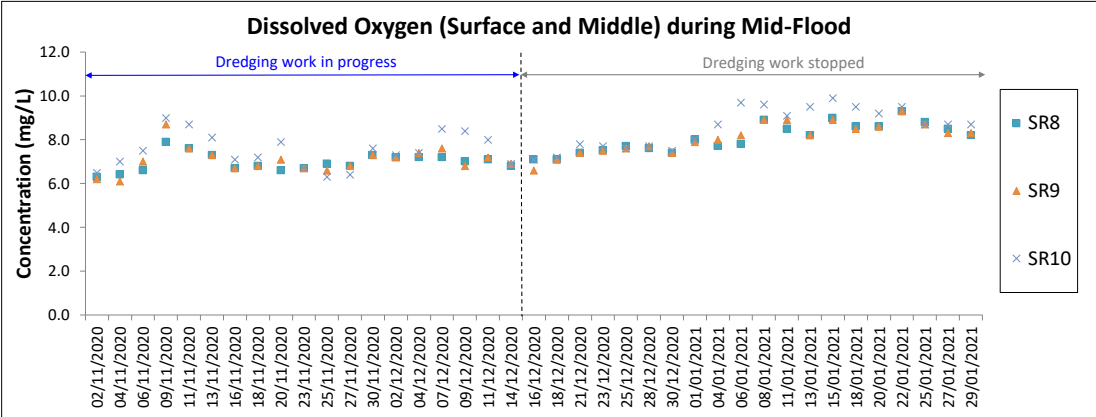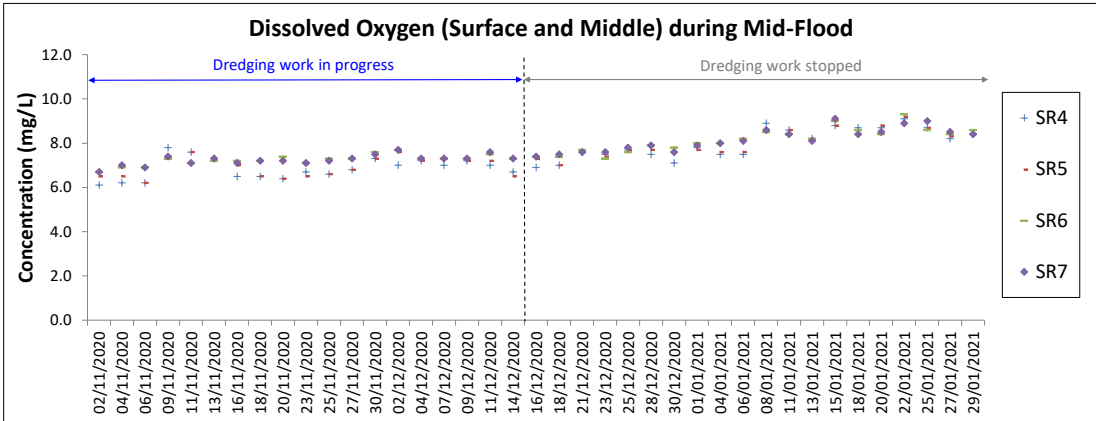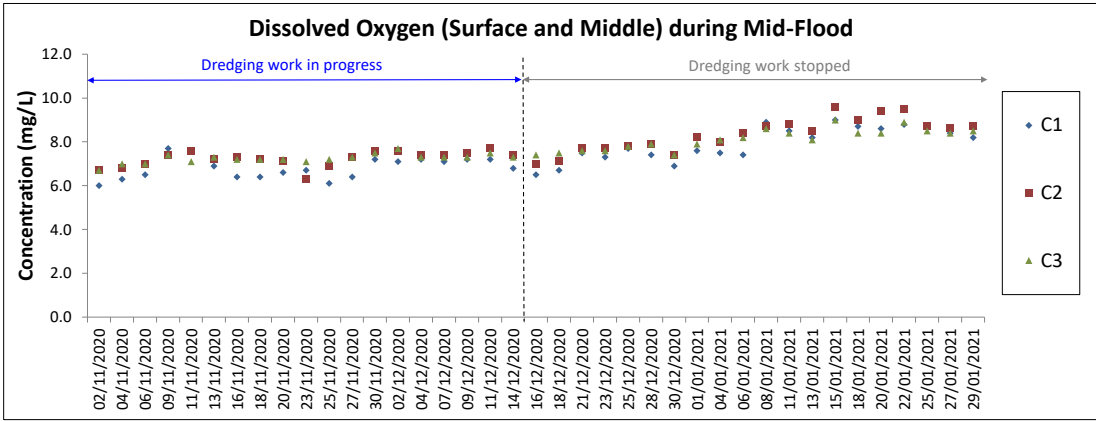

Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.



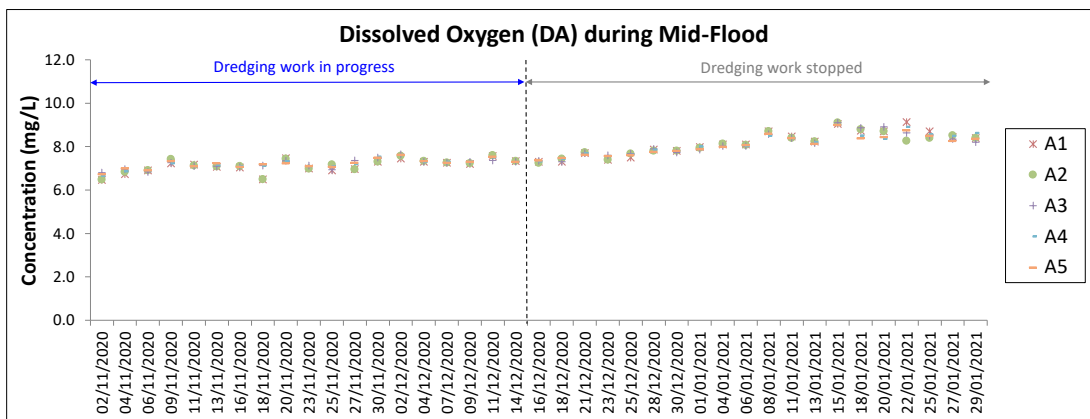
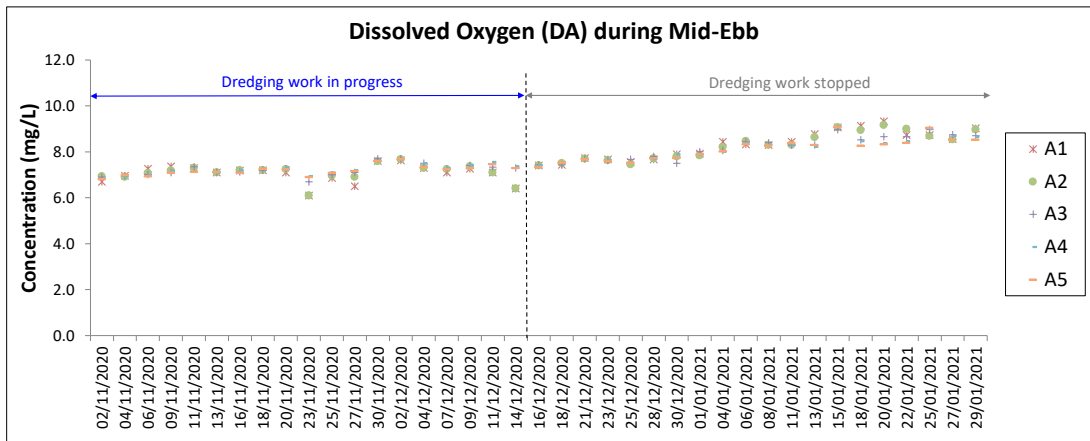


Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

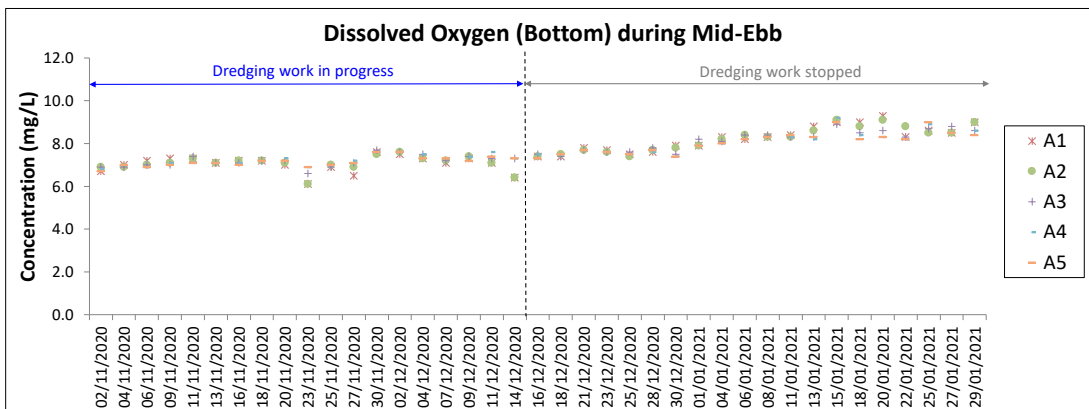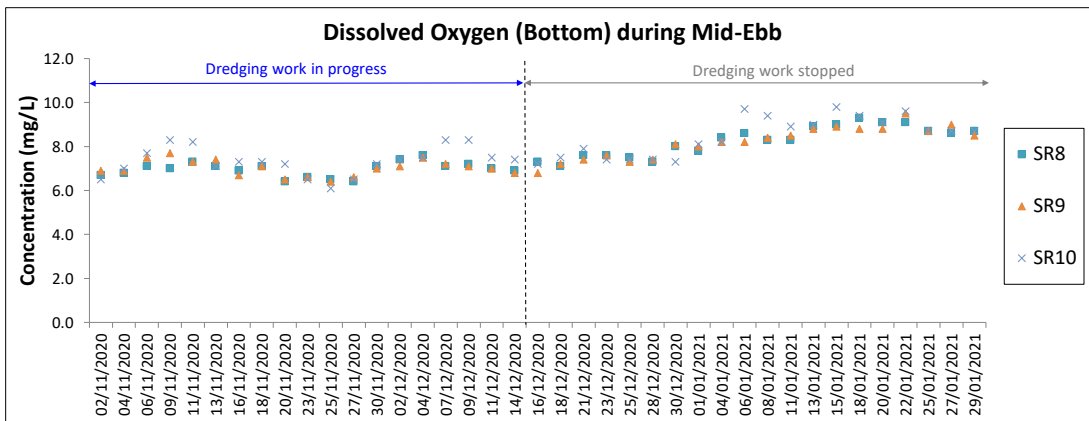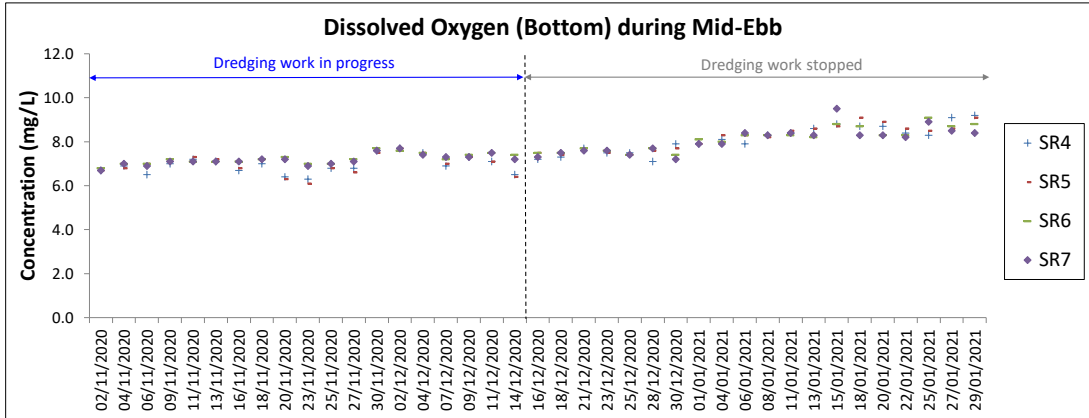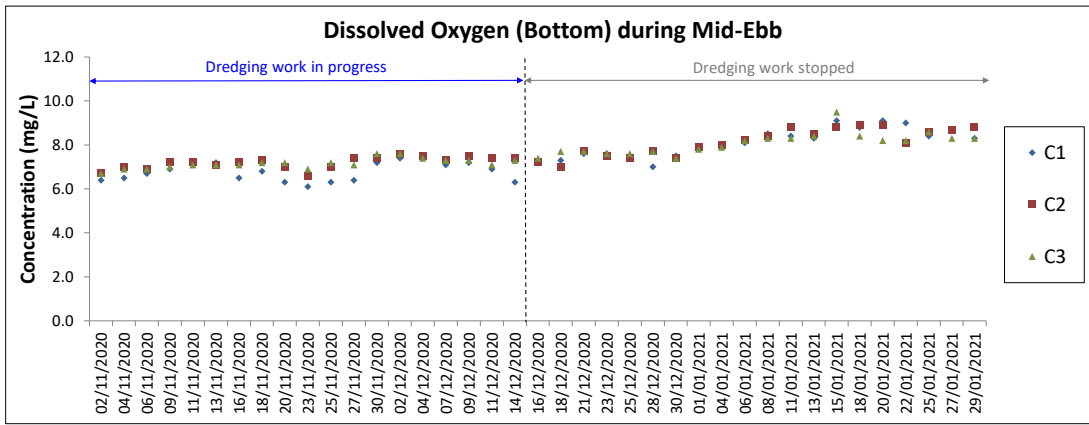





Note:

General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

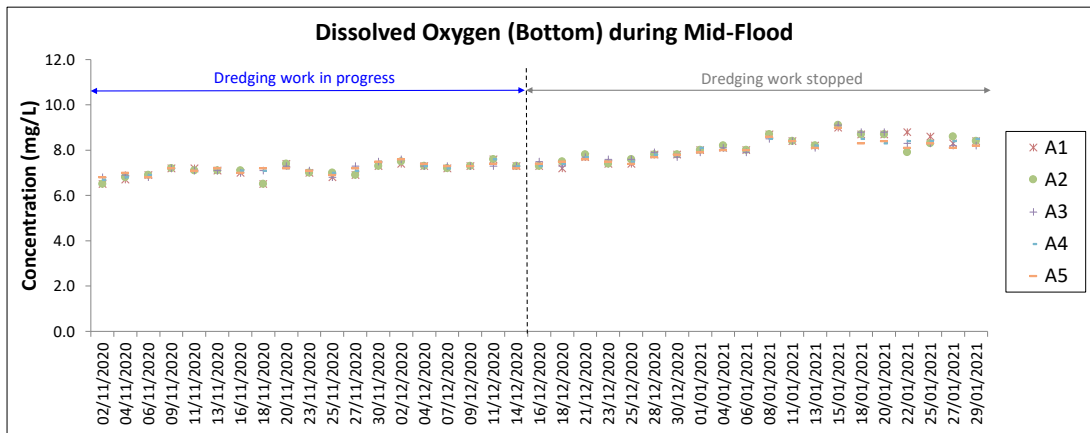
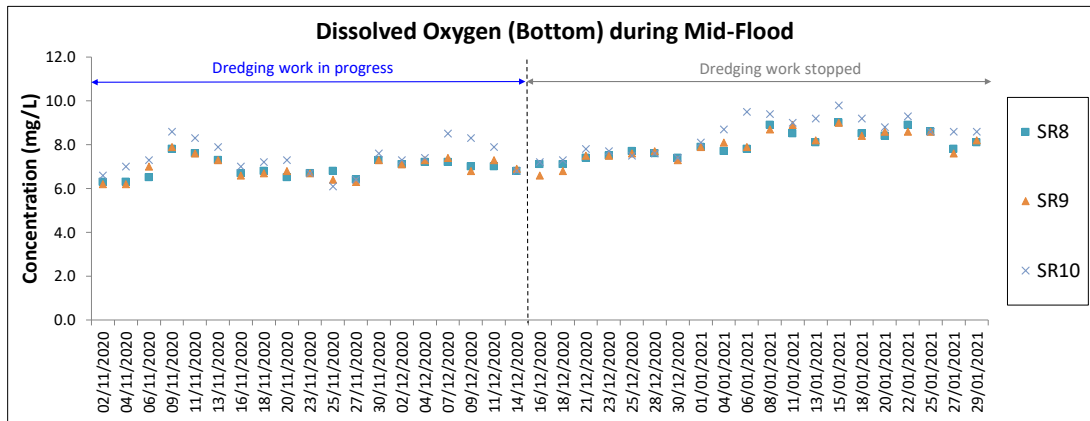
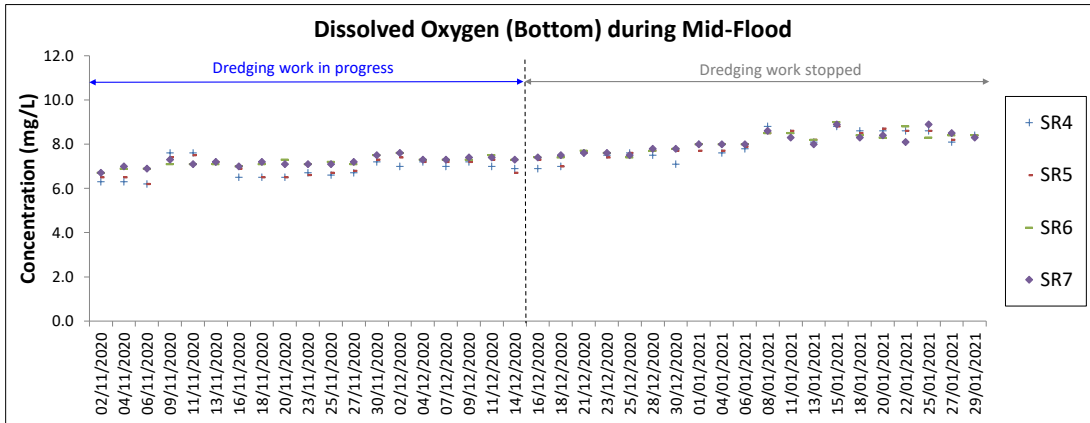
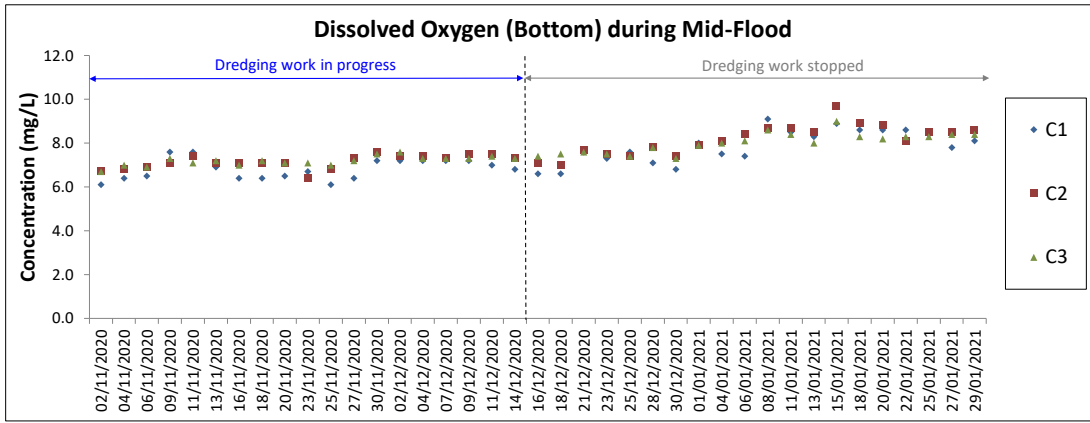


Note:




General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

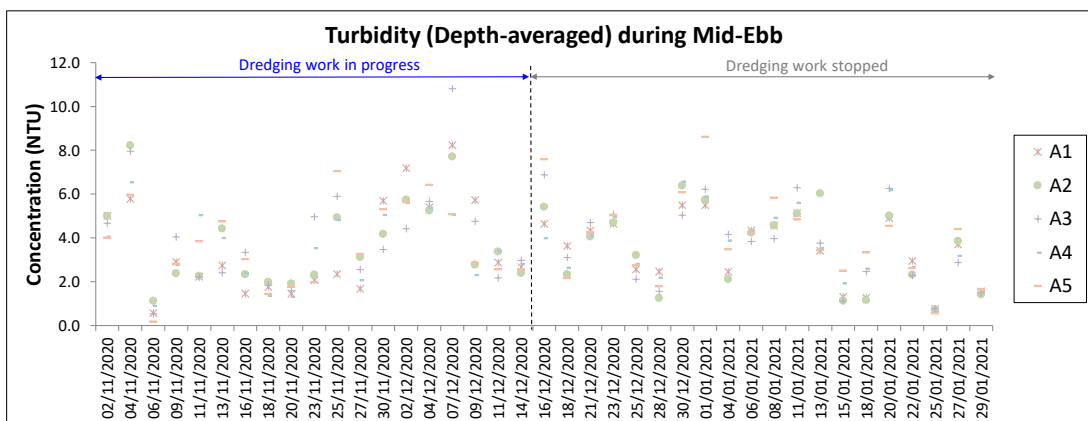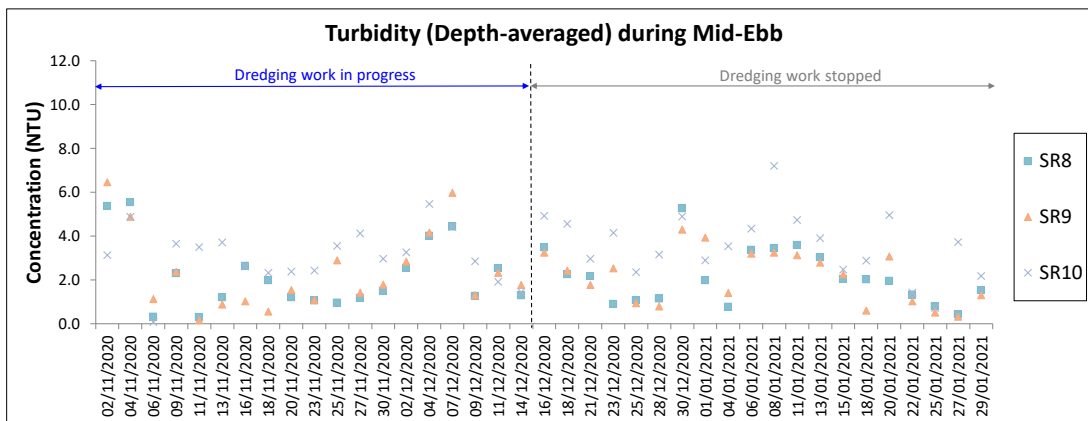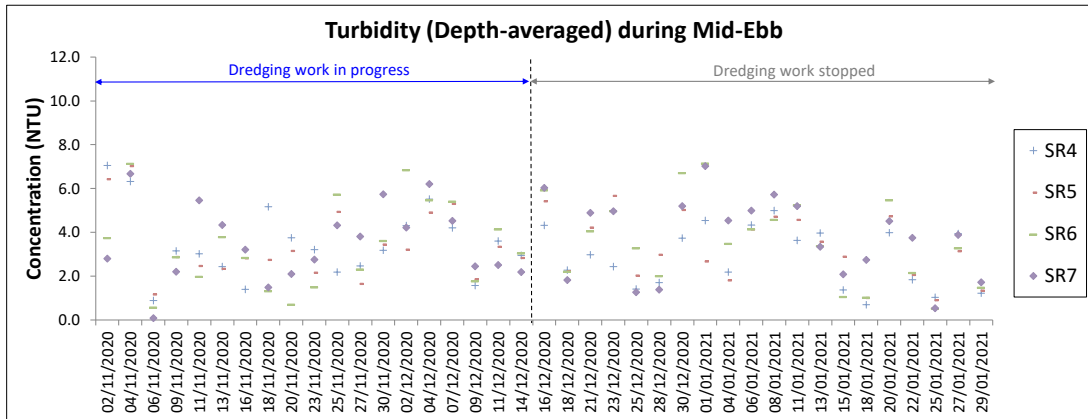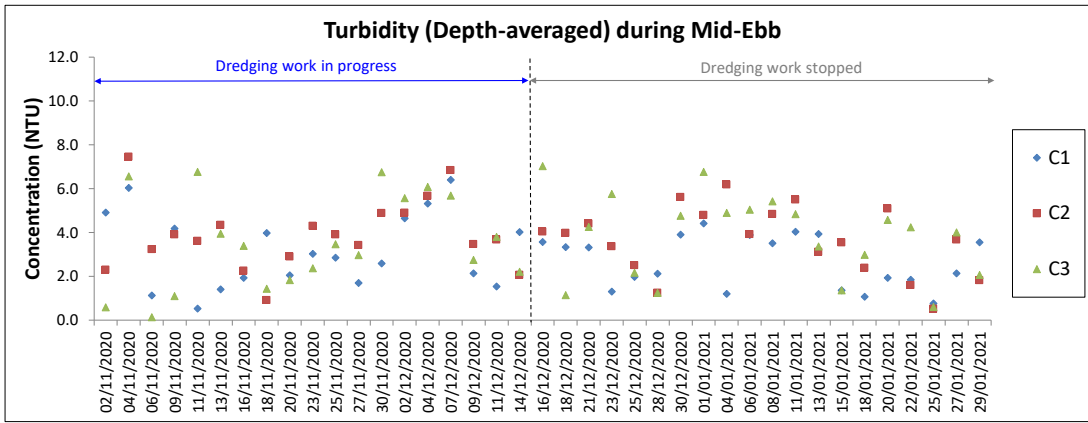




Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

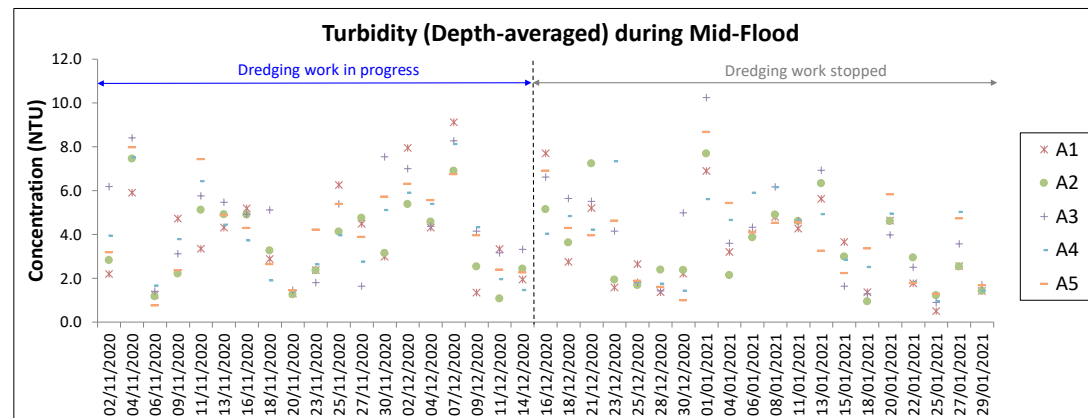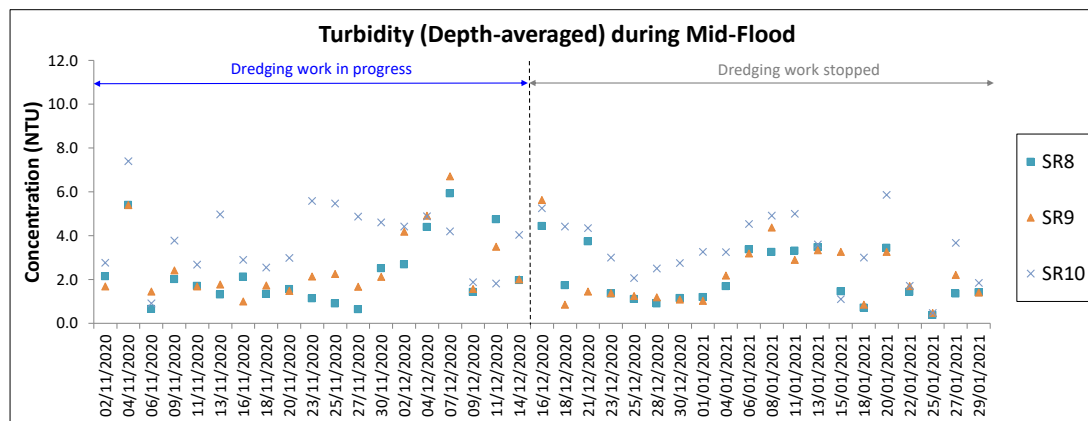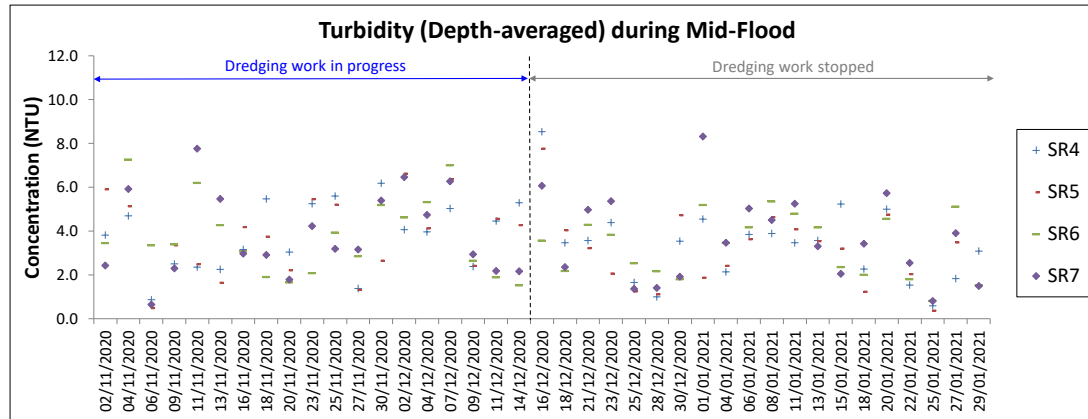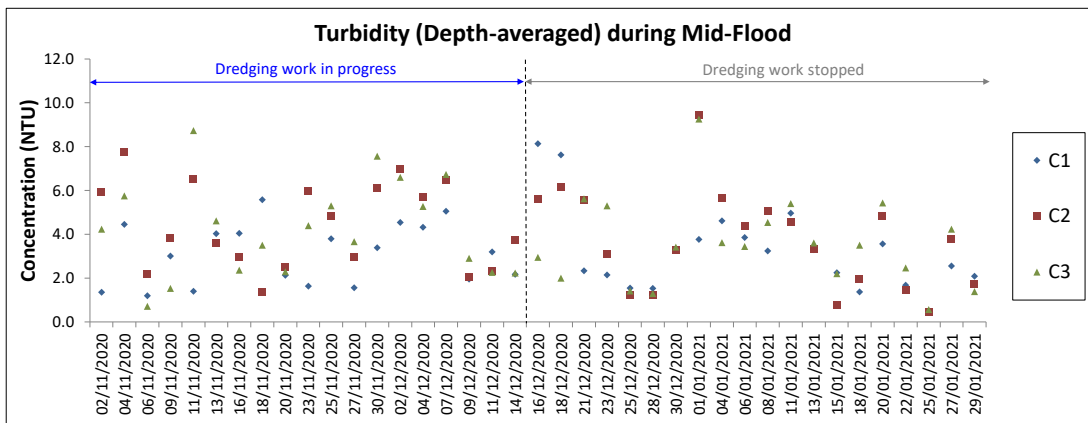


Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

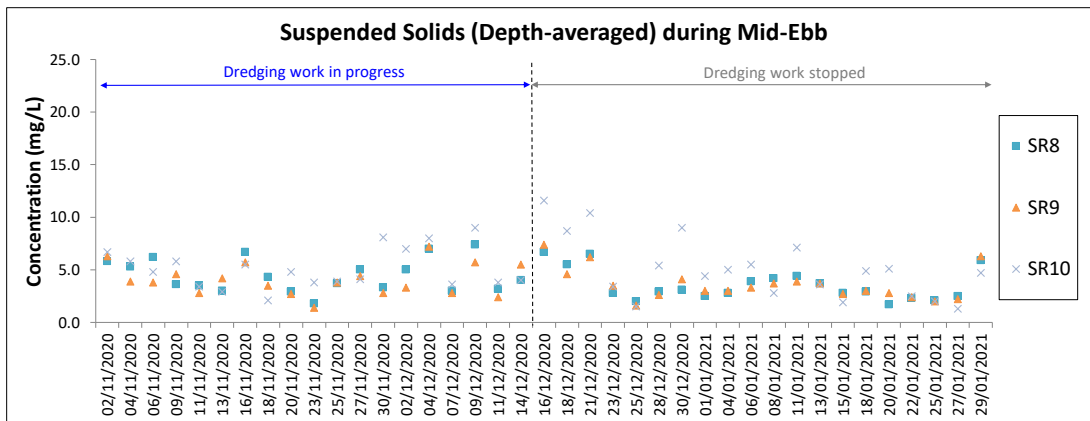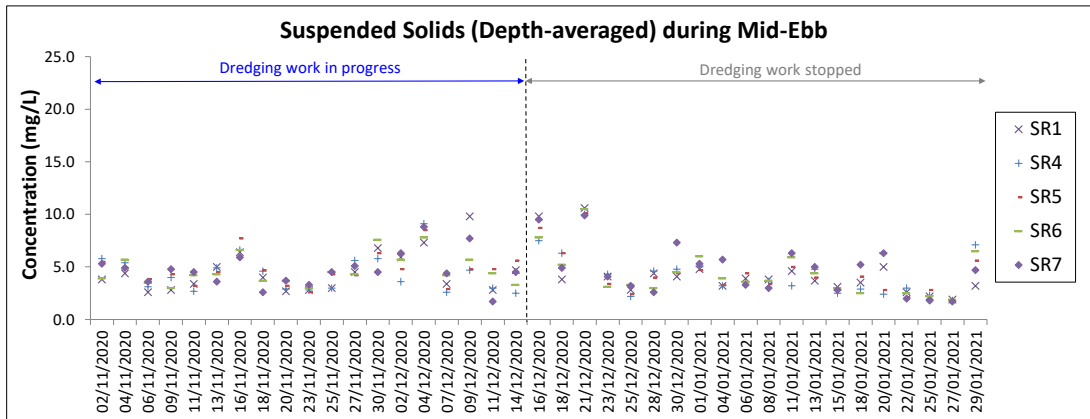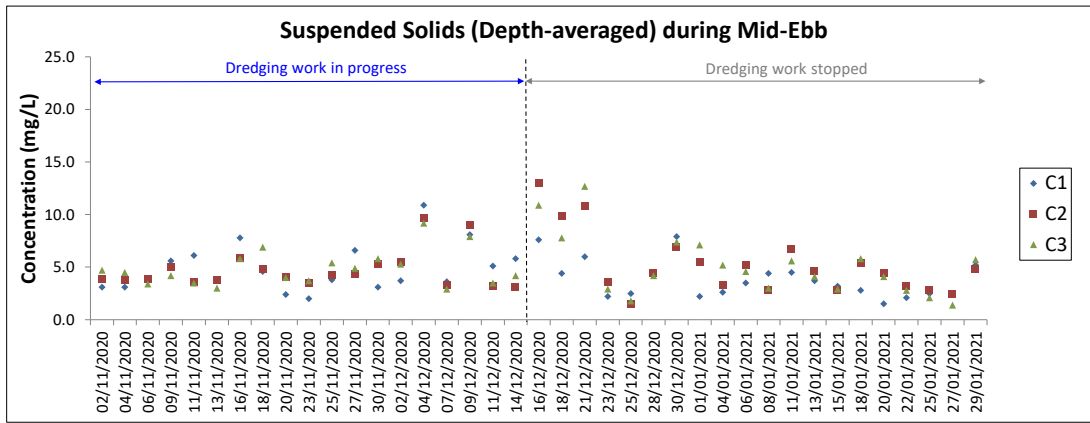

Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.

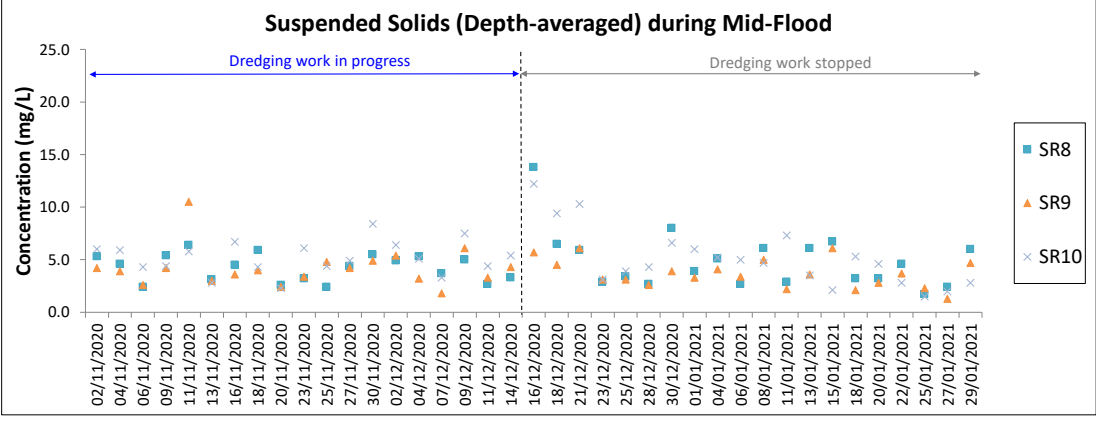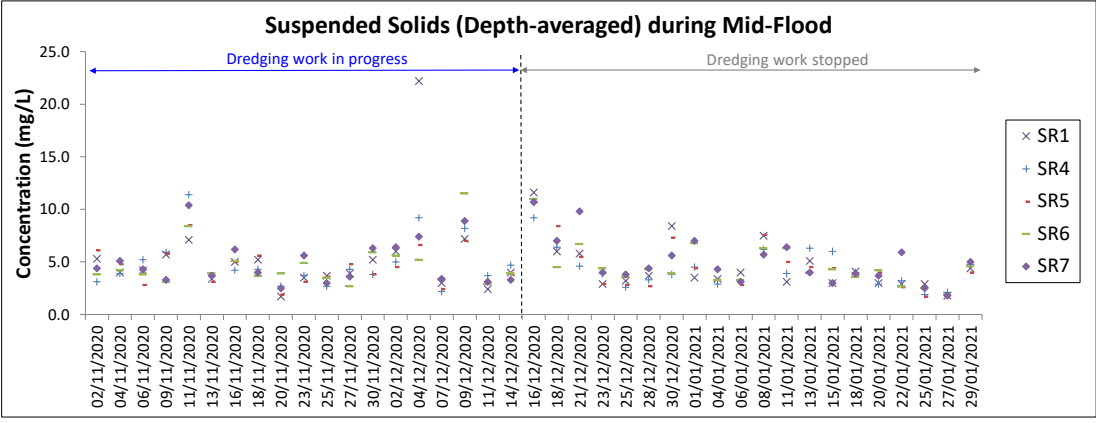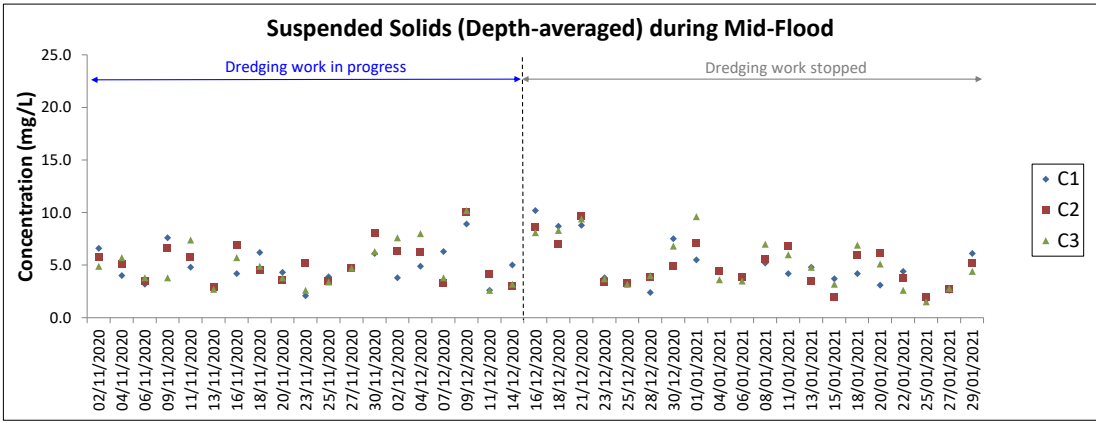

Note:
 General weather condition during monitoring ranged from sunny to rainy, with sea condition ranged from calm to rough. Detailed meteorological conditions can be referred to the corresponding Monthly Water Quality Monitoring Reports.



Annex D Alert/Event and Action Plans

D1: Event and Action Plan for Water Quality at SR Stations

Event	Action			
	ET Leader	IEC	Engineer	Contractor
Action level being exceeded by one sampling day	<ul style="list-style-type: none"> Repeat in-situ measurements to confirm findings; Inform IEC, Contractor and Engineer; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, Engineer and Contractor; Repeat in-situ measurement on next day of exceedance. 	<ul style="list-style-type: none"> Discuss with ET, Engineer and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise Engineer accordingly; Verify the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the mitigation measures; Make agreement on the mitigation measures to be implemented; Supervise the implemented of agreed mitigation measures. 	<ul style="list-style-type: none"> Identify source(s) of impact; Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and Engineer and propose mitigation measures; Implement the agreed mitigation measures
Action Level being exceeded on more than one consecutive sampling day	<ul style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Inform IEC, Contractor and Engineer; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, Engineer and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Confirm the need for reducing dredging rates as per G2. 	<ul style="list-style-type: none"> Discuss with ET, Engineer and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise Engineer accordingly; Verify the effectiveness of the implemented mitigation measures; Verify the need for reducing dredging rates as per G2. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Discuss with ET, IEC and Contractor on the effectiveness of the implemented mitigation measures; Instruct the Contractor to reduce dredging rates as per G2 if confirmed by ET and verified by IEC. 	<ul style="list-style-type: none"> Identify the source(s) of impact; Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and Engineer and propose mitigation measures to Engineer and IEC within 3 working days of notification; Implement the agreed mitigation measures; As directed by the Engineer, reduce dredging rates as per G2.

Event	Action			
	ET Leader	IEC	Engineer	Contractor
Limit Level being exceeded by one sampling day	<ul style="list-style-type: none"> Repeat in-situ measurement to confirm findings; Inform IEC, Contractor and Engineer; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, Engineer and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of limit level. 	<ul style="list-style-type: none"> Discuss with ET, Engineer and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise Engineer accordingly; Verify the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Discuss with ET, IEC and Contractor on the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Identify the source(s) of impact; Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and Engineer and propose mitigation measures to Engineer and IEC within 3 working days of notification; Implement the agreed mitigation measures.
Limit Level being exceeded by more than one consecutive sampling days	<ul style="list-style-type: none"> Inform IEC, Contractor and Engineer; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, Engineer and Contractor; Ensure mitigation measures are implemented; Confirm the need for reducing dredging rates as per D2; Increase the monitoring frequency to daily until no exceedance of limit level for two consecutive days. 	<ul style="list-style-type: none"> Discuss with ET, Engineer and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise Engineer accordingly; Verify the effectiveness of the implemented mitigation measures; Verify the need for reducing dredging rates as per D2. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Discuss with ET, IEC and Contractor on the effectiveness of the implemented mitigation measures; Instruct the Contractor to reduce dredging rates as per D2 if confirmed by ET and verified by IEC. 	<ul style="list-style-type: none"> Identify the source(s) of impact; Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and Engineer and propose mitigation measures to Engineer and IEC within 3 working days of notification; Implement the agreed mitigation measures; As directed by the Engineer, reduce dredging rates as per D2.

D2. Reduction of Maximum Allowable Hourly Dredging Rates due to Exceedances

Frequency of Exceedance	No. of Consecutive Sampling Days					
	Two	Three	Four	Five	Six	More than Six
Action Level	5%	10%	15%	20%	30%	40%
Limit Level	10%	20%	30%	40%	50%	Stop all dredging works for one week. Contractor to propose changes in dredging methods, dredging rates and mitigation measures for agreement with ET and IEC before re-initiating dredging works.

Note: Where action level followed by limit level is exceeded consecutively, the larger percentage reduction shall apply (e.g. if action level is exceeded for four consecutive days, followed immediately by two consecutive days of limit level exceedance, the percentage reduction to be applied between Day 2 and Day 6 shall be 5%, 10%, 15%, 20% and 30% respectively). Similarly, where limit level followed by action level is exceeded consecutively, the larger percentage reduction also applies as action level is inherently exceeded whenever limit level is exceeded.

D3. Alert Action Plan

The Alert Action Plan applies to exceedances of Alert levels at the near stations (A1 to A5) only. Upon identification of an exceedance of Alert level, the actions as in Alert Action Plan shall be implemented. Where applicable, the alert related actions shall proceed in parallel with the Event and Action Plan.

Action	Action By	Outcome	Follow Up Action	Follow Up Action By
1. Repeat in-situ measurement to confirm findings	ET	No exceedance in repeat measurement	No further action required	
		Exceedance identified in repeat measurement	Proceed to Action 2	
2. Check relevant SR station results	ET	No exceedance of Action or Limit Level	Notify IEC, Engineer and Contractor	ET
			Obtain and record Contractor's working methods and the status of existing mitigation measures implemented	ET
			Identify any unacceptable practice	ET, IEC, Engineer
			Rectify any unacceptable practice	Contractor
			Proceed to Action 3	
		Exceedance of Action or Limit Level	Initiate Event and Action Plan in Action or Limit Level	ET, IEC, Engineer, Contractor
		Proceed to Action 3		
3. Check for repeated cases of Outcome 2a or 2b	ET	No consecutive repeats of Outcome 2a or 2b	No further action required	
		Consecutive repeats of Outcome 2a	Review Contractor's working methods / mitigation measures and discuss with IEC, Engineer and Contractor	ET
			Identify and agree on improvements such as changes in working methods and/or additional mitigation measures	ET, IEC, Engineer, Contractor
			Implement the recommended improvements	Contractor
		Consecutive repeats of Outcome 2b	Review Alert levels and propose revised Alert levels where necessary to prevent exceedances at SR stations (due to project activities)	ET
			Verify the revised Alert levels	IEC
			Notify and agree with EPD on revised Alert levels	ET, Project Proponent

Annex E Site Audit Summary

Period: November 2020

Dates of Inspection: 6/11/2020, 11/11/2020, 16/11/2020 and 27/11/2020

Summary of Findings

General

- No environmental deficiency identified.

Water Quality & Marine Ecology

- No environmental deficiency identified.

Hazard to Life

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Period: December 2020

Dates of Inspection: 4/12/2020, 10/12/2020 and 14/12/2020 (Grab dredgers had been demobilized from the Project Site since 16/12/2020 in the reporting month.)

Summary of Findings

General

- No environmental deficiency identified.

Water Quality & Marine Ecology

- No environmental deficiency identified.

Hazard to Life

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Period: January 2021

There was no dredging work performed in the reporting month. Therefore, no weekly site audit was carried out. Independent Environmental Checker (IEC) conducted a site inspection on 25 January 2021 to audit the water quality monitoring works. The monitoring works were generally satisfactory.

Dates of Inspection: N.A.

Summary of Findings

General

- No environmental deficiency identified.

Water Quality & Marine Ecology

- No environmental deficiency identified.

Hazard to Life

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Annex F Summary of EMIS

EM&A Log Ref.	Mitigation Measures	Implementation Status
EM&A: 2.10	Dredging shall be conducted by either closed grab dredgers and/or TSHDs. The grab dredgers shall not be operating at the same time as the TSHDs.	C
EM&A: 2.10	The dredging rates for the Project shall not exceed the maximum allowable dredging rates for each respective working zone and for the respective dredging method.	C
EM&A: 2.10	Adequate clearance to the seabed shall be provided to vessel at all states of tide.	C
EM&A: 2.10	No overflow is permitted and use of lean mixture overboard (LMOB) system is prohibited.	C
EM&A: 2.10	Closed grab capacity of grab dredger should not be less than 8m ³ (except near the submarine pipeline where smaller grabs may be used).	C
EM&A: 2.10	Cage-type silt curtains (at least 10m depth) shall be deployed for grab dredgers in accordance with the Silt Curtain Deployment Plan	C
EM&A: 3.2	No dredging shall be carried out at Zone 4 of the navigation channel during the calving season for the Finless Porpoise from February to April.	C
EM&A: 3.2	As far as practicable, vessel movements to disposal grounds bypass the Finless Porpoise habitat area in southwest and east Lamma.	C
EM&A: 3.2	Implement a maximum speed limit of 10 knots in south and east Lamma waters.	C
EM&A: 3.2	All vessel operators working on the Project should be thoroughly briefed on the possible occurrence of Finless Porpoise within and in the vicinity of the Project Area and along routes to the Project Area, as well as rules for safe vessel operation around cetaceans.	C
EM&A: 5.2 & 5.3	Marine vessels should avoid traveling during berthing and unberthing of coal vessel.	C
EM&A: 5.2 & 5.3	As far as practicable, marine vessels should avoid traveling after sunset or under low visibility when the works area is near submarine pipeline.	C
EM&A: 5.2 & 5.3	Working vessel not to stay right above the submarine pipeline unless it is necessary.	C
EM&A: 5.2 & 5.3	TSHD should not lower suction pipes in close proximity of the submarine pipeline.	N/A
EM&A: 5.2 & 5.3	TSHD should not stay near the submarine pipeline unless approval is granted.	N/A
EM&A: 6.1	The number of dredgers and operation conditions specified in the applicable CNPs should be strictly followed.	C
EM&A: 7.2 & 7.3	Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation.	C
EM&A: 7.2 & 7.3	All barges and hoppers shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material.	C

EM&A Log Ref.	Mitigation Measures	Implementation Status
EM&A: 7.2 & 7.3	The Real Time Tracking and Monitoring of Vessel (RTTMV) system should be installed in hoppers/ TSHD for monitoring the mud dumping activities.	C

Remarks:

- C - Compliance with mitigation measure
- NC - Non-compliance with mitigation measure
- N/A - Not Applicable
