



**Agreement No. CE 30/2018 (EP)  
Environmental Team for Kai Tak Sports Park –  
Design and Construction**

Monthly EM&A Report for October 2020

November 2020



Home Affairs Bureau  
1/F, Block A, Kai Tak Sports Park  
Site Office, Muk Tai Street,  
Kai Tak, Kowloon

**Agreement No. CE 30/2018 (EP)**  
**Environmental Team for Kai Tak Sports Park –**  
**Design and Construction**

Monthly EM&A Report for October 2020

November 2020





## Environmental Permit No. EP-544/2017

### Kai Tak Sports Park - Investigation

### Independent Environmental Checker Verification


#### Reference Document/Plan

Document/ <del>Plan</del> to be <del>Certified</del> / Verified:	Monthly EM&A Report No. 19 (October 2020)
Date of Report:	November 2020
Date received by IEC:	10 November 2020

#### Reference EP Condition

Environmental Permit Condition:	3.4
Three hard copies and one electronic copy of the monthly EM&A Report shall be submitted to the Director within 10 working days after the end of each reporting month. The monthly EM&A Reports shall include a summary of all non-compliance with the recommendations in the approved EIA Report (Register No. AEIAR-204/2017) or this Permit. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of submission shall be provided upon request by the Director.	

#### IEC Verification

I hereby verify that the above referenced document/ <del>plan</del> complies with the above referenced condition of EP-544/2017.	
	
Ms Mandy To	Date: 11 November 2020
Independent Environmental Checker	



Environmental Permit No. EP- 544/2017

Kai Tak Sports Park – Investigation

Environmental Team Leader Certification

Reference Document /Plan

Document/ <del>Plan</del> to be Certified:	Monthly EM&A Report for October 2020
Date of Report:	November 2020
Date received by ETL:	10 November 2020

Reference EP Condition

Environmental Permit Condition:	3.4
---------------------------------	-----

Three hard copies and one electronic copy of the monthly EM&A Report shall be submitted to the Director within 10 working days after the end of each reporting month. The monthly EM&A Reports shall include a summary of all non-compliance with the recommendations in the approved EIA Report (Register No. AEIAR-204/2017) or this Permit. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of submission shall be provided upon request by the Director.

ETL Certification

I hereby certify that the above reference document complies with the above referenced condition of EP-544/2017.

Mr Sunny Chan  
Environmental Team Leader

Date: 11 November 2020

# Contents

Executive summary	1
<b>1 Introduction</b>	<b>4</b>
1.1 Background	4
1.2 Project Organisation	5
1.3 Works Area and Construction Programme	5
1.4 Construction Works undertaken during the Reporting Period	6
<b>2 Air Quality Monitoring</b>	<b>7</b>
2.1 Introduction	7
2.2 Monitoring Parameters, Frequency and Duration	7
2.3 Monitoring Locations	7
2.4 Monitoring Action and Limit Levels	7
2.5 Monitoring Schedule for the Reporting Period	8
2.6 Monitoring Equipment	8
2.7 Monitoring Methodology	8
2.8 Monitoring Results	9
2.9 Wind Data	9
<b>3 Noise Monitoring</b>	<b>10</b>
3.1 Introduction	10
3.2 Monitoring Parameters, Frequency and Duration	10
3.3 Monitoring Locations	10
3.4 Action and Limit Levels	11
3.5 Monitoring Schedule for the Reporting Period	11
3.6 Monitoring Equipment	11
3.7 Monitoring Methodology	11
3.8 Monitoring Results	12
<b>4 Environmental Site and Audit</b>	<b>13</b>
4.1 Site Inspection	13
4.2 Advice on the Solid and Liquid Waste Management Status	14
4.3 Environmental Licenses and Permits	15
4.4 Implementation Status of Environmental Mitigation Measures	15
4.5 Summary of Exceedance of the Environmental Quality Performance Limit	15
4.6 Summary of Complaints, Notification of Summons and Successful Prosecution	15
<b>5 Future Key Issues</b>	<b>17</b>
5.1 Construction Programme for the Coming Months	17

5.2	Environmental Site Inspection and Monitoring Schedule for the Next Reporting Period	17
6	Conclusions	18
6.1	Conclusions	18

## Figures

Figure 2.1: Location of Air Quality Monitoring Stations

Figure 3.1: Location of Noise Monitoring Stations

## Appendices

Appendix A. Project Organization for Environmental Works

Appendix B. Location of Works Areas

Appendix C. Construction Programme

Appendix D. Event and Action Plan

Appendix E. Environmental Site Inspection and Monitoring Schedule

Appendix F. Calibration Certificates

Appendix G. Monitoring Data and Graphical Plots (Air Quality and Noise)

Appendix H. Wind Data

Appendix I. Waste Flow Table

Appendix J. Environmental Licences and Permits

Appendix K. Environmental Mitigation Measures Implementation Status

Appendix L. Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

Appendix M. Complaint Investigation Report

## Tables

Table 1.1:	Contact Information of Key Personnel	5
Table 2.1:	Air Quality Monitoring Parameters, Frequency and Duration	7
Table 2.2:	Construction Dust Monitoring Locations	7
Table 2.3:	Action and Limit Levels for 1-hour TSP	8
Table 2.4:	1-hour TSP Monitoring Equipment	8
Table 2.5:	Summary of 1-hour TSP Monitoring Results During the Reporting Period	9
Table 3.1:	Noise Monitoring Parameters, Frequency and Duration	10
Table 3.2:	Construction Noise Monitoring Locations	10
Table 3.3:	Action and Limit Level for Construction Noise	11
Table 3.4:	Noise Monitoring Equipment	11
Table 3.5:	Summary of Construction Noise Monitoring Results During the Reporting Period	12
Table 4.1:	Summary of Site Inspections and Recommendations	13
Table 4.2:	Summary of Complaints in the Reporting Month	15
Table 5.1:	Construction Activities for the Next Reporting Period	17
Table D.1:	Event and Action Plan for Construction Air Quality (Action Level)	



Table D.2: Event and Action Plan for Construction Air Quality (Limit Level)

Table D.3: Event and Action Plan for Construction Noise

Table E.1: Site Inspection and Monitoring Schedule for October 2020

Table E.2: Tentative Site Inspection and Monitoring Schedule for November 2020

Table J.1: Summary of Environmental Licences and Permits Status (KTSP)

Table J.2: Summary of Environmental Licences and Permits Status (H/O Development)

Table L.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

# Executive summary

The Project – hereby meaning the Designated Project (Items O.6 and O.7 Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO)), comprising the “Kai Tak Sports Park” (KTSP) project and the Hotel and Office (H/O) Development of NKIL 6607 adjoining the KTSP – is located in the Kai Tak Development (KTD) area in Kowloon.

An EIA Report for the Project (Register No. AEIAR-204/2017) was approved by the Environmental Protection Department (EPD) on 6 January 2017. The current Environmental Permit (EP) for the Project, namely No. EP-544/2017, was issued on 8 September 2017. These documents are available through the EIA Ordinance Register. The Project construction works commenced on 8 April 2019.

In February 2019, Mott MacDonald Hong Kong Limited was appointed by the Home Affairs Bureau (HAB) as the Environmental Team (ET) to implement the Environmental Monitoring & Audit (EM&A) programme for the construction phase and first year of operation of the Project in accordance with the approved EM&A Manual.

This is the 19<sup>th</sup> Monthly EM&A Report for the construction phase of the Project which summaries findings of the EM&A programme during the reporting period from 1 to 31 October 2020.

## Key Construction Works in the Reporting Period

A summary of construction activities undertaken during the reporting period is presented below:

### KTSP

- Ground investigation works;
- Pile cap construction;
- Piling works (Percussive piling, Socket H piling and Bored piling);
- Mobilization; and
- Concreting and excavation.

### H/O Development

- Sheet piling; and
- Socket H piling

## Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken by ET in accordance with the approved EM&A Manual. A summary of the monitoring activities during the reporting period is presented below:

Activity	Monitoring Locations	Date
Air Quality Monitoring (1-hour TSP)	AMS1, AMS2	3, 9, 15, 21, 27 Oct 2020
Noise Monitoring ( $L_{eq}$ (30 min))	NMS1, NMS2	3, 9, 15, 21, 27 Oct 2020
Weekly environmental site inspections	-	7, 14, 20, 28 Oct 2020
Landscape and visual site inspections	-	7, 20 Oct 2020

## Breaches of Action and Limit Levels

### *Air Quality*

There was no breach of Action or Limit Levels for Air Quality (1-hr TSP) during the reporting month.

### *Noise*

There was no breach of Action or Limit Levels for noise level during the reporting month.

## Complaint Log

There was one complaint in relation to the environmental impact received during the reporting month.

### Summary of Complaints in the reporting month

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
6 Oct 2020	11 Sep 2020	<p>- Complaint of soil/muddy water at To Kwa Wan Typhoon Shelter on 10 September 2020.</p> <p>- Please closely monitor the effluent of your wastewater treatment plants, provide sufficient wastewater treatment capacity and implement practicable measures to prevent discharge of muddy water including surface run-off from your site. Please ensure the works comply with all relevant environmental legislations.</p>	<ol style="list-style-type: none"><li>1. Regular monitoring of water quality at effluent discharge on site.</li><li>2. Silt curtain has been provided and kept good maintenance near barging point.</li><li>3. Sedimentation tank has been provided for treatment and temporary storage of the wastewater.</li><li>4. Regular sludge removal of the sedimentation tank has been conducted .</li></ol>	8 Oct 2020

## Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during this reporting period.

## Reporting Changes

There was no reporting change during the reporting period.

## **Future Key Issues**

The future key issues to be undertaken in the upcoming month are:

### **KTSP**

- Ground investigation works;
- Pile cap construction;
- Piling works (Percussive piling, Socket H piling and Bored piling);
- Mobilization; and
- Concreting and excavation.

### **H/O Development**

- Sheet piling; and
- Socket H piling.

# 1 Introduction

## 1.1 Background

The Project – hereby meaning the Designated Project (Items O.6 and O.7 Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO)), comprising the “Kai Tak Sports Park” (KTSP) project and the Hotel and Office (H/O) Development of NKIL 6607 adjoining the KTSP – is located in the Kai Tak Development (KTD) area in Kowloon.

The key construction works of the Project include:

### (i) KTSP project

- a. a multi-purpose Main Stadium with a spectator capacity of around 50,000;
- b. a Public Sports Ground, with a spectator capacity of around 5,000;
- c. an Indoor Sports Centre with a multi-purpose main arena with a seating capacity of up to 10,000 and an ancillary sports hall with a seating capacity of 500;
- d. retail and dining outlets with a gross floor area (GFA) of about 57,000 square metres (m<sup>2</sup>), a bowling centre with 40 lanes and a health and wellness centre with about 2,500 m<sup>2</sup> GFA;
- e. more than 8 hectares of public open space including landscaped deck structures across Shing Kai Road, passive amenities and park features, outdoor ball courts; and
- f. ancillary facilities such as car parks, toilets, changing rooms, etc.

### (ii) H/O Development

- g. an office development;
- h. a 300-room hotel with a GFA of about 16,000 m<sup>2</sup>; and
- i. ancillary facilities such as retails, car parks, etc.

In February 2019, Mott MacDonald Hong Kong Limited (MMHK) was commissioned by the Home Affairs Bureau (HAB) under Agreement No. CE 30/2018 (EP) to undertake the Environmental Team (ET) services for carrying out the Environmental Monitoring & Audit (EM&A) programme during the construction phase and first year of operation of the Project in accordance with the approved Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-204/2017), EM&A Manual (including any subsequent amendments) and EP (including any subsequent variations of it and/or any further environmental permit issued under the EIAO). The current EP (No. EP-544/2017) was issued by EPD on 8 September 2017.

This is the 19<sup>th</sup> Monthly EM&A Report summarising the key findings of the construction phase EM&A programme from 1 to 31 October 2020 (the “reporting period”) and is submitted to fulfil Condition 3.4 of the EP.

## 1.2 Project Organisation

The organisation chart and lines of communication with respect to the on-site environmental management structure of the key personnel are shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

**Table 1.1: Contact Information of Key Personnel**

Party	Position	Name	Telephone	Fax
Project Proponent (Home Affairs Bureau)	Project Director (Sports Park)	Victor Tai	3586 3403	3586 0591
Supervising Officer's Representative (Home Affairs Bureau)	Senior Engineer	Keith Man	3586 3149	3586 0591
Environmental Team (Mott MacDonald Hong Kong Limited)	Environmental Team Leader	Sunny Chan	2828 5962	2827 1823
	Deputy Environmental Team Leader	Henry Leung	2828 5876	2827 1823
Independent Environmental Checker (ERM Hong Kong Limited)	Independent Environmental Checker	Mandy To	2271 3000	2723 5660
Contracted Party (Kai Tak Sports Park Limited)	Senior Project Manager	Michael Wong	3552 5003	2845 9295
	Senior Environmental Engineer	Hiko Law	3552 5013	3552 5099
<b>Hotel and Office Development</b>				
Project Manager (Sanon Limited)	Senior Group Project Director	David Lee	2910 8368	2815 9949
	Project Manager	William Chan	2910 8363	2815 9949
Project Architect (P&T Architects & Engineers Limited)	Project Architect	Patrick Chan	2832 7205	-
Contractor (CR Construction Company Limited)	Contractor	Math Chan	3950 5714	-
24-hour Community Liaison Hotline	-	-	5587 6112	-

## 1.3 Works Area and Construction Programme

The construction works commenced on 8 April 2019. The works area of the Project is shown in **Appendix B**. The Construction Works Programme of the Project is provided in **Appendix C**.

## 1.4 Construction Works undertaken during the Reporting Period

A summary of construction activities undertaken during this reporting period is presented below:

### **KTSP**

- Ground investigation works;
- Pile cap construction;
- Piling works (Percussive piling, Socket H piling and Bored piling);
- Mobilization; and
- Concreting and excavation.

### **H/O Development**

- Sheet piling; and
- Socket H piling.

## 2 Air Quality Monitoring

### 2.1 Introduction

In accordance with the EM&A Manual of the Project, baseline 1-hour Total Suspended Particulates (TSP) levels at air quality monitoring stations AMS1 and AMS2 were established. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days.

### 2.2 Monitoring Parameters, Frequency and Duration

**Table 2.1** summarises the monitoring parameters, frequency and duration of impact noise monitoring.

**Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration**

Parameter	Frequency and Duration
1-hour TSP	3 times every six-days

### 2.3 Monitoring Locations

According to the EM&A Manual, a total of five air quality monitoring stations are identified for impact monitoring. Of these, three air sensitive receivers are planned residential use and were not available for baseline monitoring; the same three are also currently not available for impact monitoring.

**Table 2.2** describes the impact air quality monitoring stations and **Figure 2.1** shows their locations.

**Table 2.2: Construction Dust Monitoring Locations**

Monitoring Station	Location	Status
AMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Air Sensitive Receiver
AMS2	Sky Tower, Podium of Tower 7	Existing Air Sensitive Receiver
AMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Air Sensitive Receiver
AMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Planned Air Sensitive Receiver
AMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Air Sensitive Receiver

During the reporting period, monitoring locations AMS1 and AMS2 were set up at the proposed locations for impact monitoring.

Permission on setting up and carrying out impact monitoring works at AMS3, AMS4 and AMS5 will be sought once each respective development is completed and occupied.

### 2.4 Monitoring Action and Limit Levels

The Action and Limit Levels for 1-hr TSP are provided in **Table 2.3**.



**Table 2.3: Action and Limit Levels for 1-hour TSP**

Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1 – Hong Kong Society for the Blind Workshop, Roof Floor	283	500
AMS2 – Sky Tower, Podium of Tower 7	280	500
AMS3 - Kai Tak Area 2B Site 4 (2B4) (residential use)	287*	500
AMS4 - Kai Tak Area 1K Site 3 (1K3) (residential use)	287*	500
AMS5 - Kai Tak Area 1L Site 3 (1L3) (residential use)	287*	500

\*Remarks: the Action Level for AMS3, AMS4 and AMS5 were derived from an alternative monitoring station AMS3-4-5 during the baseline monitoring.

The event and action plan is provided in **Appendix D**.

If exceedance(s) at these stations is/are recorded by the ET of the Project, it will carry out an investigation and findings will be reported in the monthly EM&A Report.

## 2.5 Monitoring Schedule for the Reporting Period

The schedule for air quality monitoring at AMS1 and AMS2 in the reporting period is presented in **Appendix E**.

## 2.6 Monitoring Equipment

Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. The brand(s) and model(s) of the equipment used for air quality monitoring stations AMS1 and AMS2 under this Project are given in **Table 2.4**.

**Table 2.4: 1-hour TSP Monitoring Equipment**

Equipment	Brand	Model No.
Portable direct reading dust meter	Sibata Digital Dust Monitor	LD-3B (S/N: 235780 & 6Z7784)

## 2.7 Monitoring Methodology

### Field Monitoring

The measuring procedures of the 1-hour TSP dust meter are in accordance with the Manufacturer’s Instruction Manual as follows:

- Turn the power on.
- Close the air collecting opening cover.
- Push the “TIME SETTING” switch to [BG].
- Push “START/STOP” switch to perform background measurement for 6 seconds.
- Turn the knob at SENSI ADJ position to insert the light scattering plate.
- Leave the equipment for 1 minute upon “SPAN CHECK” is indicated in the display.
- Push “START/STOP” switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- Pull out the knob and return it to MEASURE position.
- Setting time period of 1 hour for the 1-hour TSP measurement.

- Push “START/STOP” to start the 1-hour TSP measurement.
- Regular checking of the time period setting to ensure monitoring time of 1 hour.

**Maintenance and Calibration**

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are given in **Appendix F**.

**2.8 Monitoring Results**

The monitoring results for 1-hour TSP at AMS1 and AMS2 are summarized in **Table 2.5**. Detailed impact air quality monitoring results are presented in **Appendix G**.

**Table 2.5: Summary of 1-hour TSP Monitoring Results During the Reporting Period**

Monitoring Station	Average, $\mu\text{g}/\text{m}^3$	Min, $\mu\text{g}/\text{m}^3$	Max, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1	58	30	79	283	500
AMS2	60	39	76	280	500

There was no Action and Limit Level exceedance of 1-hr TSP level recorded at station AMS1 and AMS2 by the ET during the reporting period.

**2.9 Wind Data**

Wind data at Kai Tak automatic weather station collected from the Hong Kong Observatory (HKO) were used for the air quality monitoring and they are shown in **Appendix H**. It is considered that the wind data obtained at the existing Kai Tak wind station are representative of the Project area and could be used for undertaking the construction phase baseline and impact air quality monitoring programme for the Project.

The proposed use of the existing wind data from Kai Tak automatic weather station collected from HKO for wind data collection instead of setting up wind monitoring equipment near the monitoring stations was proposed by ET and agreed by IEC in accordance with the requirements as stated in Section 3.4.7 of the EM&A Manual of the Project.

## 3 Noise Monitoring

### 3.1 Introduction

In accordance with the EM&A Manual, impact noise monitoring was conducted at least once per week for each noise monitoring location during the construction phase of the Project.

### 3.2 Monitoring Parameters, Frequency and Duration

**Table 3.1** summarises the monitoring parameters, frequency and duration of impact noise monitoring.

**Table 3.1: Noise Monitoring Parameters, Frequency and Duration**

Parameter	Frequency and Duration
30-minutes measurement at each monitoring station between 0700 and 1900 on normal weekdays (Monday to Saturday). L <sub>eq</sub> , L <sub>10</sub> and L <sub>90</sub> would be recorded.	At least once per week

### 3.3 Monitoring Locations

According to the approved EM&A Manual, a total of seven noise monitoring stations were identified for the impact monitoring locations. Of these, five noise sensitive receivers are planned residential use (NMS1A, NMS2A, NMS3, NMS4 and NMS5) and were not available for baseline monitoring; the same five are also currently not available for impact monitoring.

**Table 3.2** describes the details of the monitoring stations and **Figure 3.1** shows the locations of noise monitoring stations.

**Table 3.2: Construction Noise Monitoring Locations**

Monitoring Station	Location Description	Status
NMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Noise Sensitive Receiver
NMS2	Sky Tower, Podium of Tower 7	Existing Noise Sensitive Receiver
NMS1A	Sung Wong Toi Road Public Housing Site	Planned Noise Sensitive Receiver
NMS2A	Sung Wong Toi Road CDA Site (mixed use)	Planned Noise Sensitive Receiver
NMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Noise Sensitive Receiver
NMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Planned Noise Sensitive Receiver
NMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Noise Sensitive Receiver

During the reporting period, monitoring locations NMS1 and NMS2 were set up at the proposed locations for impact monitoring.

Since NMS1A & NMS2A are planned (i.e. not existing) noise sensitive receivers, noise monitoring should be carried out initially at NMS1 and NMS2 respectively before the population intake of the planned developments. Once the planned developments are completed and occupied, NMS1A shall replace NMS1, while NMS2A shall replace NMS2. It is proposed that

the baseline noise level and Limit Level at NMS1A and NMS2A will be the same as those derived from the baseline monitoring data recorded at NMS1 and NMS2 respectively.

Permission on setting up and carrying out impact monitoring works at NMS3, NMS4 and NMS5 will be sought once each respective development is completed and occupied.

### 3.4 Action and Limit Levels

The Action and Limit Levels for construction noise are defined in **Table 3.3**.

**Table 3.3: Action and Limit Level for Construction Noise**

Monitoring Station	Time Period	Action Level	Limit Level
NMS1 NMS2	0700 – 1900 hours on normal weekdays	When one documented complaint is received	75 dB(A)

The event and action plan is provided in **Appendix D**.

If exceedance(s) at these stations is/are recorded by the ET of the Project, it will carry out an investigation and findings will be reported in the monthly EM&A Report.

### 3.5 Monitoring Schedule for the Reporting Period

The schedule for noise monitoring in the reporting period is presented in **Appendix E**.

### 3.6 Monitoring Equipment

Noise monitoring was performed using sound level meters at each designed monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment used for noise monitoring under this Project is given in **Table 3.4**.

**Table 3.4: Noise Monitoring Equipment**

Equipment	Brand	Model No.
Integrated Sound Level Meter	Rion	NL-52 (serial no. 01010406)
Acoustic Calibrator	LARSON DAVIS	CAL200 (S/N 11334)

### 3.7 Monitoring Methodology

- Façade and Free Field measurements were made at the monitoring locations.
- For Façade measurement, the microphone hear of the head level meter was positioned 1m exterior of the noise sensitive façade and lowered sufficiently so that the building’s external wall acts as a reflecting surface.
- For free field, the microphone of the Sound Level Meter was set at least 1.2 m above the ground.
- A correction of +3dB(A) was made for free field measurement.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting: A
  - time weighting: Fast

- time measurement: 30-minute intervals (between 0700-1900 on normal weekdays)
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid and repeated after the re-calibration or repair of the equipment.
- During the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.
- Noise measurements were not made in presence of fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s.

**Maintenance and Calibration**

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The sound level meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix F**.

**3.8 Monitoring Results**

The monitoring results for construction noise are summarized in **Table 3.5**. Detailed impact noise monitoring results and relevant graphical plots are presented in **Appendix G**.

**Table 3.5: Summary of Construction Noise Monitoring Results During the Reporting Period**

Monitoring Station	Measured Noise Level $L_{eq}$ (30 mins), dB(A)			Limit Level
	Average	Min	Max	
NMS1	71	69	73	75
NMS2	69	68	70	75

No noise exceedances were recorded at stations NMS1 and NMS2 by ET during the reporting period.

## 4 Environmental Site and Audit

### 4.1 Site Inspection

Site inspections were carried out by ET on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the Project. Key observations were recorded in the site inspection checklist and passed to the Contracted Party together with the appropriate recommended mitigation measures where necessary. During the reporting period, site inspections were carried out on 7, 14, 20, 28 October 2020. Joint IEC site inspections were carried out 20 and 28 October 2020.

Bi-weekly landscape and visual site audit was carried out on 7 and 20 October 2020. The landscape and visual audit have been audited by Registered Landscape Architect (RLA). No major observations of landscape and visual impact were identified. The result findings were summarised in **Appendix K**.

Key observations during the site inspections are described in **Table 4.1**.

**Table 4.1: Summary of Site Inspections and Recommendations**

Inspection Date	Key Observations	Recommendations / Actions	Close-Out Date / Status
<b>Kai Tak Sports Park</b>			
7 Oct 2020	Accumulation of stagnant water was observed at southern site. (zone 20).	The contractor was reminded to provide temporary water pump if necessary.	14 Oct 2020
14 Oct 2020	Accumulation of stagnant water from air conditioner was observed at northern site. (Zone 2)	The contractor was reminded to clear the stagnant water.	20 Oct 2020
14 Oct 2020	Dust emission from dry surface at northern site was observed. (zone 1)	The contractor was reminded to provide regular water spraying to maintain wet surface.	20 Oct 2020
14 Oct 2020	Leakage of site runoff from hoarding boundary near southern gate no. 1 was observed	The contractor was reminded to fix the leakage at the hoarding boundary.	20 Oct 2020
14 Oct 2020	Mixing of plastic bottle and metal in the recycling tanks was observed. (Zone 18)	The contractor was reminded to sort out the plastic and metal properly for recycling.	20 Oct 2020
14 Oct 2020	A generator with faded colour NRMM label was observed at southern site (Zone 19)	The contractor was reminded to replace the NRMM label for the generator.	20 Oct 2020
20 Oct 2020	Dry haul road at northern site (zone 5) and southern site (zone 20) was observed.	The contractor was reminded to provide regular water spraying to maintain wet surface for dust control.	28 Oct 2020
20 Oct 2020	A generator with faded colour NRMM label at northern site (zone 3)	The contractor was reminded to replace the NRMM label.	28 Oct 2020

20 Oct 2020	A stockpile without covering was observed at northern site (zone 2).	The contractor was reminded to provide covering for stockpile on site.	28 Oct 2020
28 Oct 2020	Accumulation of stockpiles without covering was observed at northern site (zone 8).	The contractor was reminded to provide covering for stockpile on site.	4 Nov 2020
28 Oct 2020	Breaking work without water spraying and noise mitigation measure was observed at northern site. (zone 6).	The contractor was reminded to provide air and noise mitigation measure for breaking works on site.	4 Nov 2020
28 Oct 2020	Dry surface at piling area near southern gate No. 2 was observed. (zone 15)	The contractor was reminded to provide water spray to maintain wet surface to minimise dust emission.	4 Nov 2020
28 Oct 2020	Chemical containers without drip tray were observed at southern site. (zone 16)	The contractor was reminded to store the chemical container properly.	4 Nov 2020
<b>Hotel and Office Development</b>			
14 Oct 2020	Mud from vehicles leaving site entrance was observed.	The contractor was reminded to ensure no mud was carrying outside the site area by provide sufficient vehicle wheel washing.	20 Oct 2020
14 Oct 2020	Chemical container without drip tray was observed.	The contractor was reminded to provide drip tray for the chemical container.	20 Oct 2020
20 Oct 2020	Transfer of cement not in enclosed system was observed.	The contractor was reminded to ensure the cement works to be carried out in enclosed system to minimise dust emission. Also, regular maintenance of filter for cement mixing work should be maintained to prevent dust emission.	28 Oct 2020

## 4.2 Advice on the Solid and Liquid Waste Management Status

### KTSP

The Contracted Party was registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting was carried out on site. Sufficient numbers of receptacles were provided for general refuse collection and sorting. Excavated inert C&D materials were reused to minimise the disposal of C&D waste to public fill.

The Contracted Party was reminded to maintain on site waste sorting and recording system and maximize reuse / recycling of C&D wastes, whenever these are generated.

### H/O Development

Construction and demolition (C&D) material sorting was carried out on site. Sufficient numbers of receptacles were provided for general refuse collection and sorting. Excavated inert C&D materials were designated for on temporary site storage and collected for the disposal to public fill.

The Contractor was reminded to maintain on site waste sorting and maximize reuse / recycling of C&D wastes, whenever these are generated.

The monthly summary of waste flow table is detailed in **Appendix I**.

### 4.3 Environmental Licenses and Permits

The valid environmental licenses and permits for the Project during the reporting period are summarized in **Appendix J**.

### 4.4 Implementation Status of Environmental Mitigation Measures

In response to the site audit findings, the Contracted Party carried out corrective actions.

A summary of the environmental mitigation measures implementation status is presented in **Appendix K**. Most of the necessary mitigation measures were implemented properly.

### 4.5 Summary of Exceedance of the Environmental Quality Performance Limit

#### Air Quality

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1 and AMS2 during the reporting period.

#### Noise

No Action and Limit Level exceedances of noise level was recorded at NMS1 and NMS2 during the reporting period.

### 4.6 Summary of Complaints, Notification of Summons and Successful Prosecution

#### Complaints

There was one complaint received in relation to the environmental impact during the reporting month.

**Table 4.2: Summary of Complaints in the Reporting Month**

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
6 Oct 2020	11 Sep 2020	- Complaint of soil/muddy water at To Kwa Wan Typhoon Shelter on 10 September 2020. - Please closely monitor the effluent of your wastewater treatment plants, provide sufficient wastewater treatment capacity and implement practicable measures to prevent discharge	1. Regular monitoring of water quality at effluent discharge on site. 2. Silt curtain has been provided and kept good maintenance near barging point. 3. Sedimentation tank has been provided for treatment and temporary storage of the wastewater. 4. Regular sludge removal of the	8 Oct 2020



---

of muddy water including surface run-off from your site. Please ensure the works comply with all relevant environmental legislations.	sedimentation tank has been conducted .
---	---

---

Details of the complaint investigation is shown in **Appendix M**.

#### **Notification of Summons and Successful Prosecution**

No notification of summons or prosecutions was received during the reporting period.

Statistics on notifications of summons and successful prosecutions are summarized in **Appendix L**.

## 5 Future Key Issues

### 5.1 Construction Programme for the Coming Months

As informed by the Contracted Party, the major construction activities for the next reporting period (November 2020) are summarized in **Table 5.1**.

**Table 5.1: Construction Activities for the Next Reporting Period**

Site Area	Description of Activities
<ul style="list-style-type: none"><li>• Kai Tak Sports Park</li></ul>	<ul style="list-style-type: none"><li>• Ground investigation works;</li><li>• Pile cap construction;</li><li>• Piling works (Percussive piling, Socket H piling and Bored piling);</li><li>• Mobilization; and</li><li>• Concreting and excavation.</li></ul>
<ul style="list-style-type: none"><li>• Hotel and Office Development</li></ul>	<ul style="list-style-type: none"><li>• Sheet piling works; and</li><li>• Socket H piling.</li></ul>

### 5.2 Environmental Site Inspection and Monitoring Schedule for the Next Reporting Period

The tentative schedule for weekly site inspection and monitoring for air quality and noise for the next reporting period is provided in **Appendix E**.

## 6 Conclusions

### 6.1 Conclusions

#### General

The construction works for the Project commenced on 8 April 2019.

The ET of the Project has implemented the air quality and noise environmental impact monitoring under the construction phase EM&A programme during the reporting period.

#### Breaches of Action and Limit Levels

##### *Air Quality*

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1 and AMS2 during the reporting period.

##### *Noise*

No Action and Limit Level exceedances of noise level was recorded at NMS1 and NMS2 during the reporting period.

#### Environmental Site Inspections

Environmental site inspections were carried out four times during the reporting period. Recommendations on remedial actions were given to the Contracted Party for the deficiencies identified during the site inspections.


#### Complaints

There was one complaint received in relation to the environmental impact during the reporting period.

#### Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

# Figures

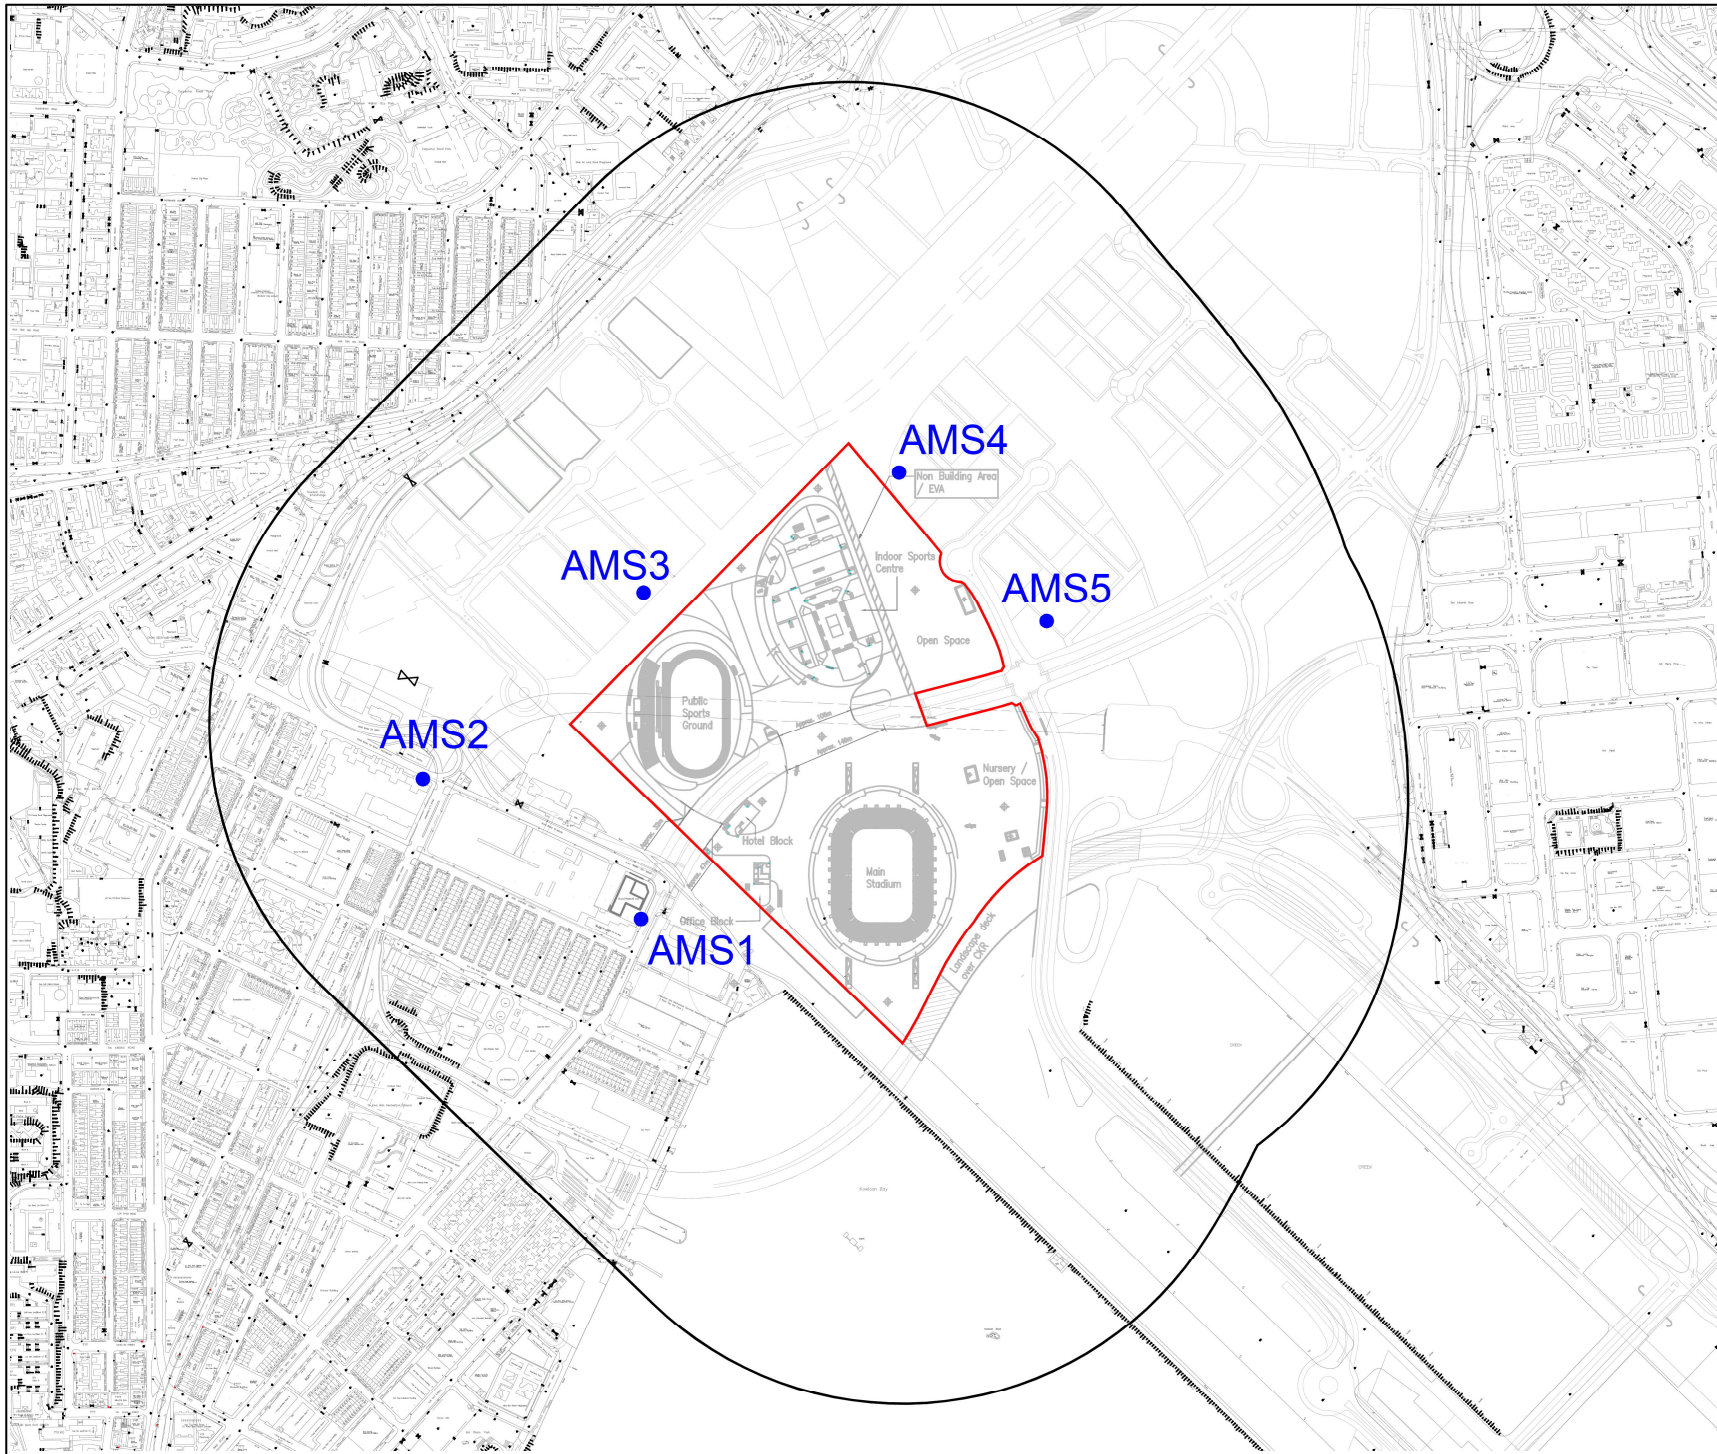

Key Plan

Notes:

1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATES SYSTEM.
3. PIPE AND BOX CULVERT SIZES ARE SHOWN IN MILLIMETERS

Key to symbols:

**LEGEND:**

- Project Site
- 500m from Site Boundary
- AMS1 • Air Monitoring Station 1

Rev	Date	Drawn	Description	Ch'g'd	App'd

**M**  
**MOTT**  
**MACDONALD**


3/F, Mapletree Bay Point  
348 Kowloon Tong Road  
Kowloon, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2827 1659  
W mottmac.com

Client

Project

Figure 2.1  
Location of Air Quality Monitoring Stations

Designed		Eng check	
Drawn		Consultation	
Dwg check		Approved	
Scale at A3	Status	Rev	
Drawing Number			

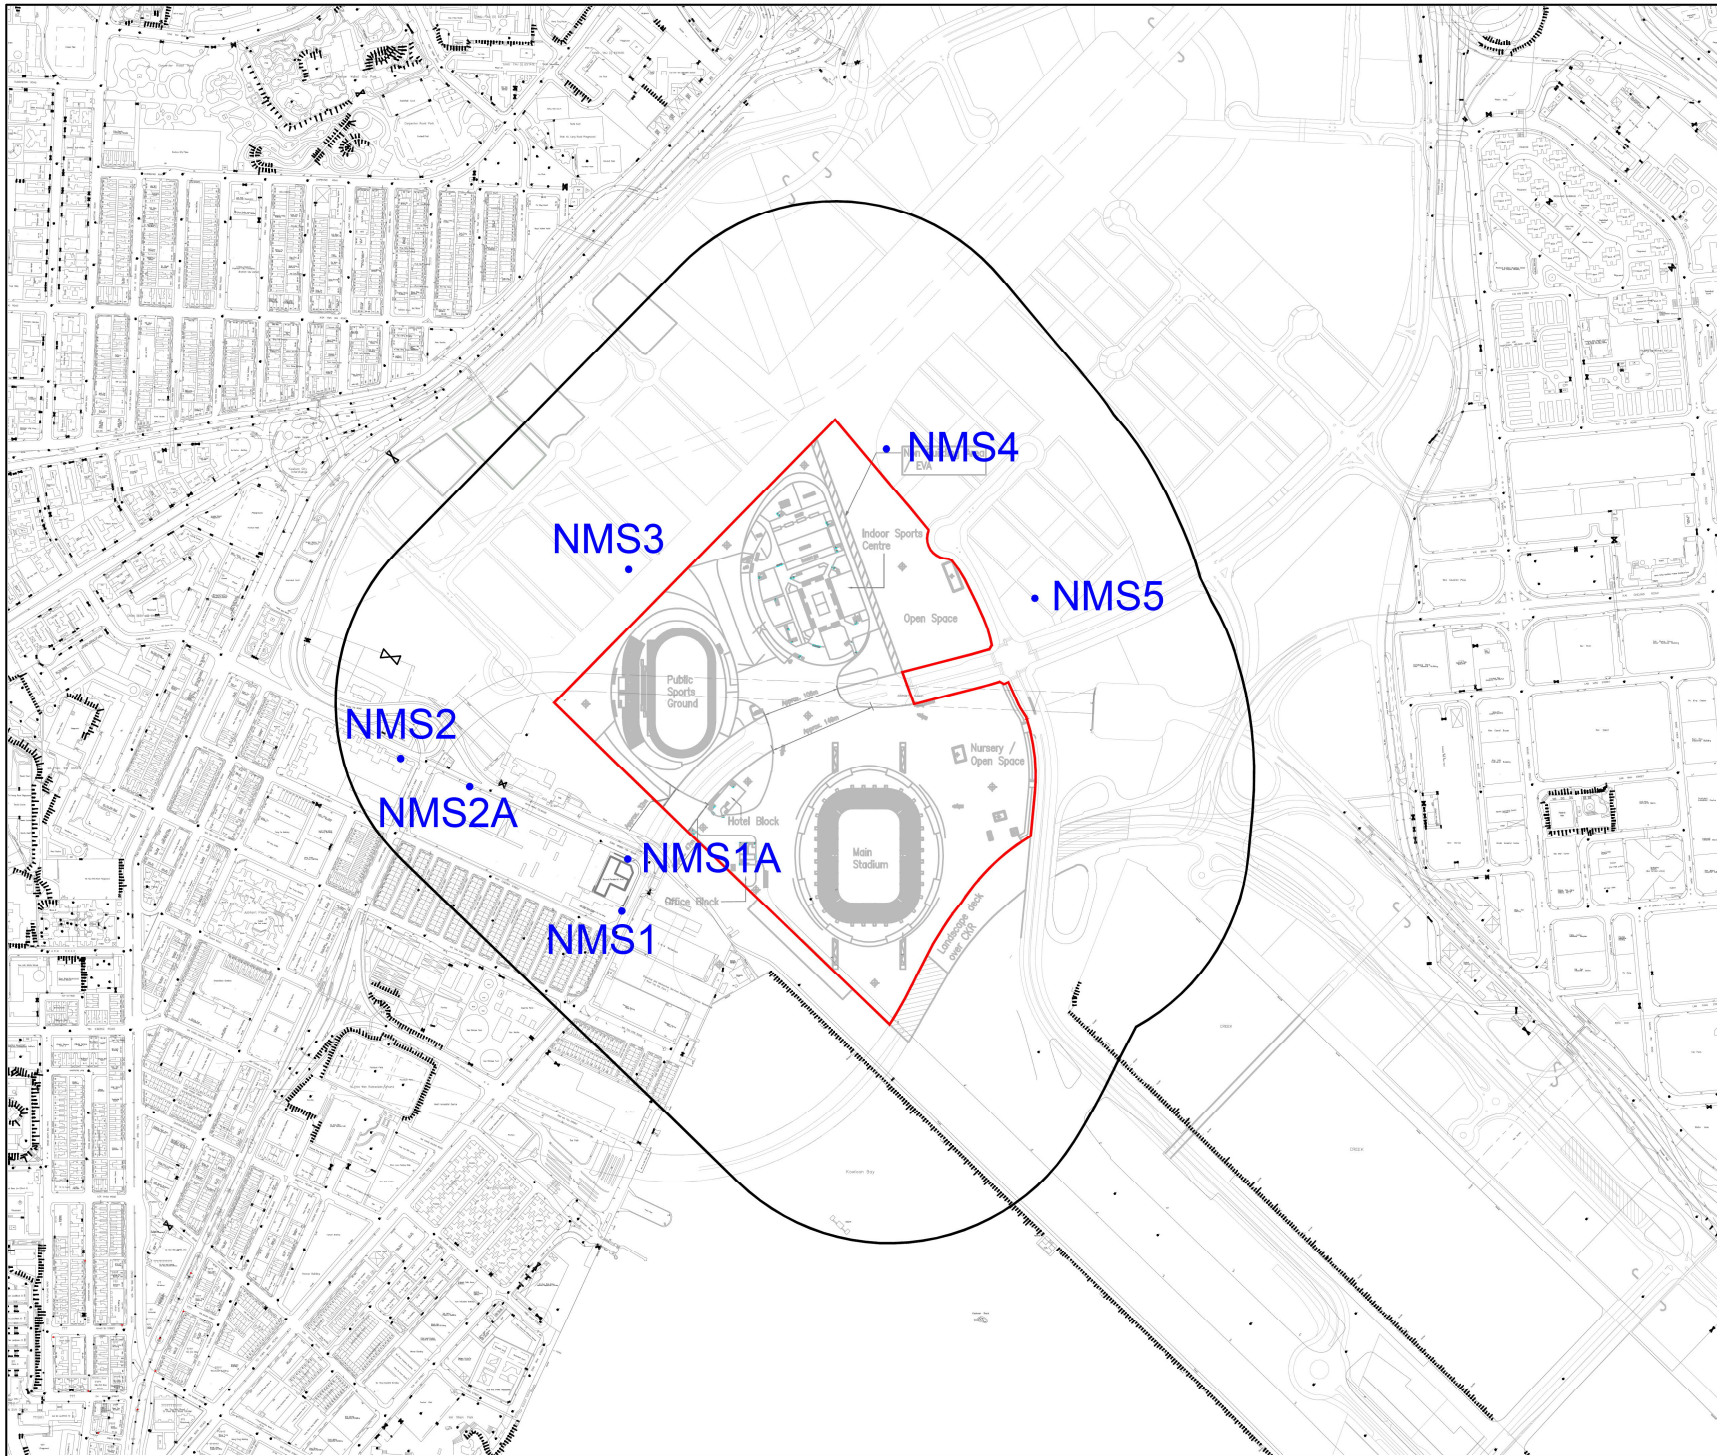

Key Plan

- Notes:
1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
  2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATE SYSTEM.
  3. PIPE AND BOX DIA/VERT SIZES ARE SHOWN IN MILLIMETERS

Key to symbols:

**LEGEND:**

- Project Site
- 300m from Site Boundary
- NMS1 • Construction Noise Monitoring Station 1

Rev	Date	Drawn	Description	Ch'g'd	App'd

**M M**  
**MOTT MACDONALD**

Client

3/F, Maple Tree Bay Point  
348 Kwun Tong Road  
Kwun Tong, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2827 1650  
W mottmac.com

Project


**Figure 3.1**  
**Location of Noise Monitoring Stations**

Designed		Eng check	
Drawn		Consultation	
Dwg check		Approved	
Scale at A3	Status		Rev

Drawing Number

# Appendix A. Project Organization for Environmental Works


# Project Organisation for Environmental Works

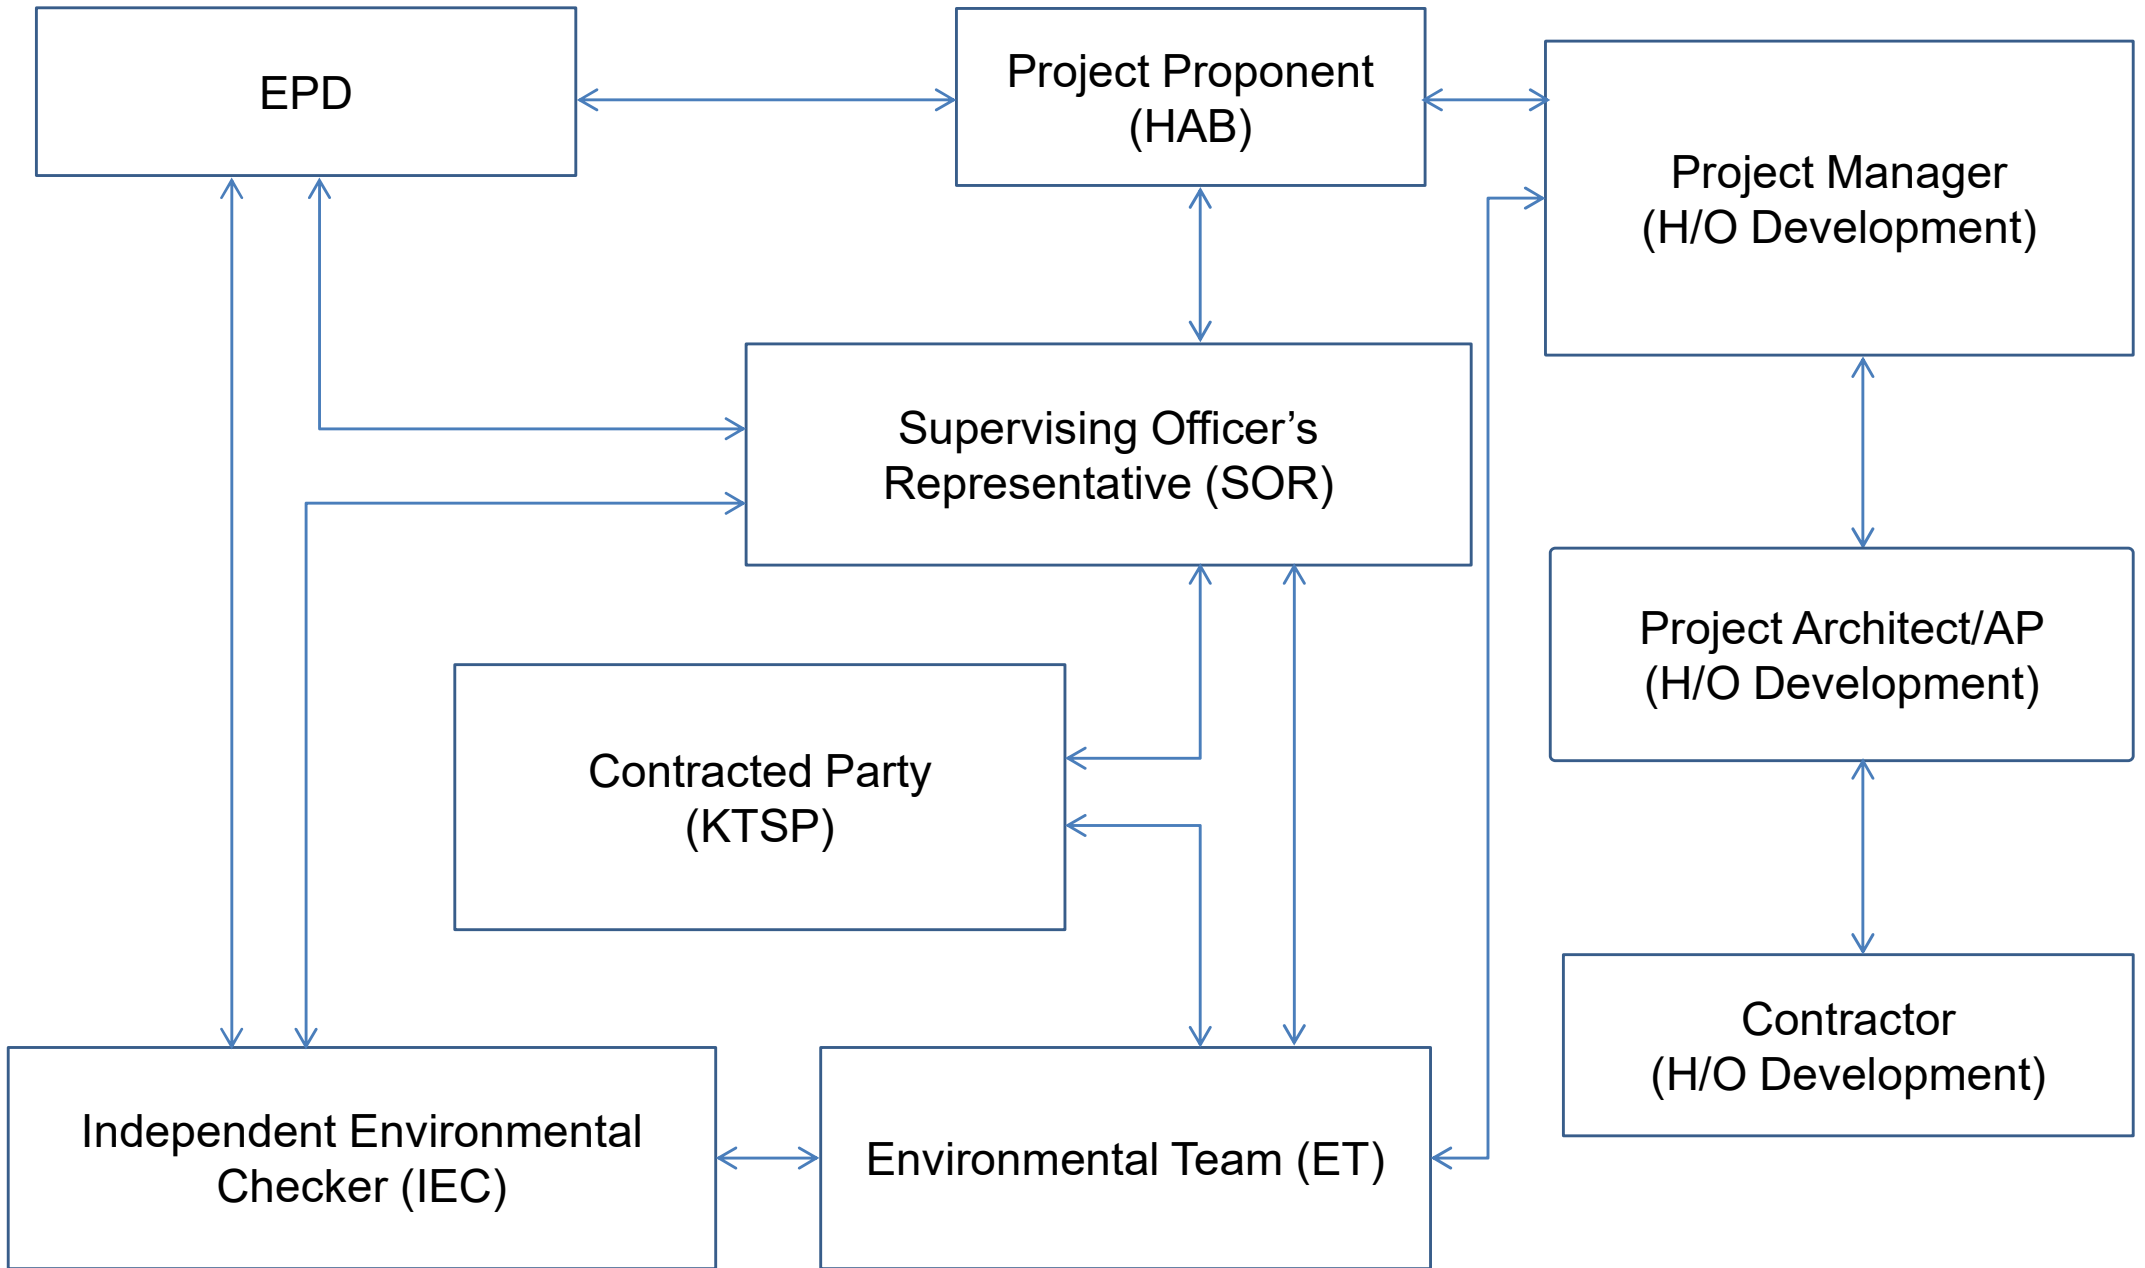

Line of communication



## Appendix B. Location of Works Areas

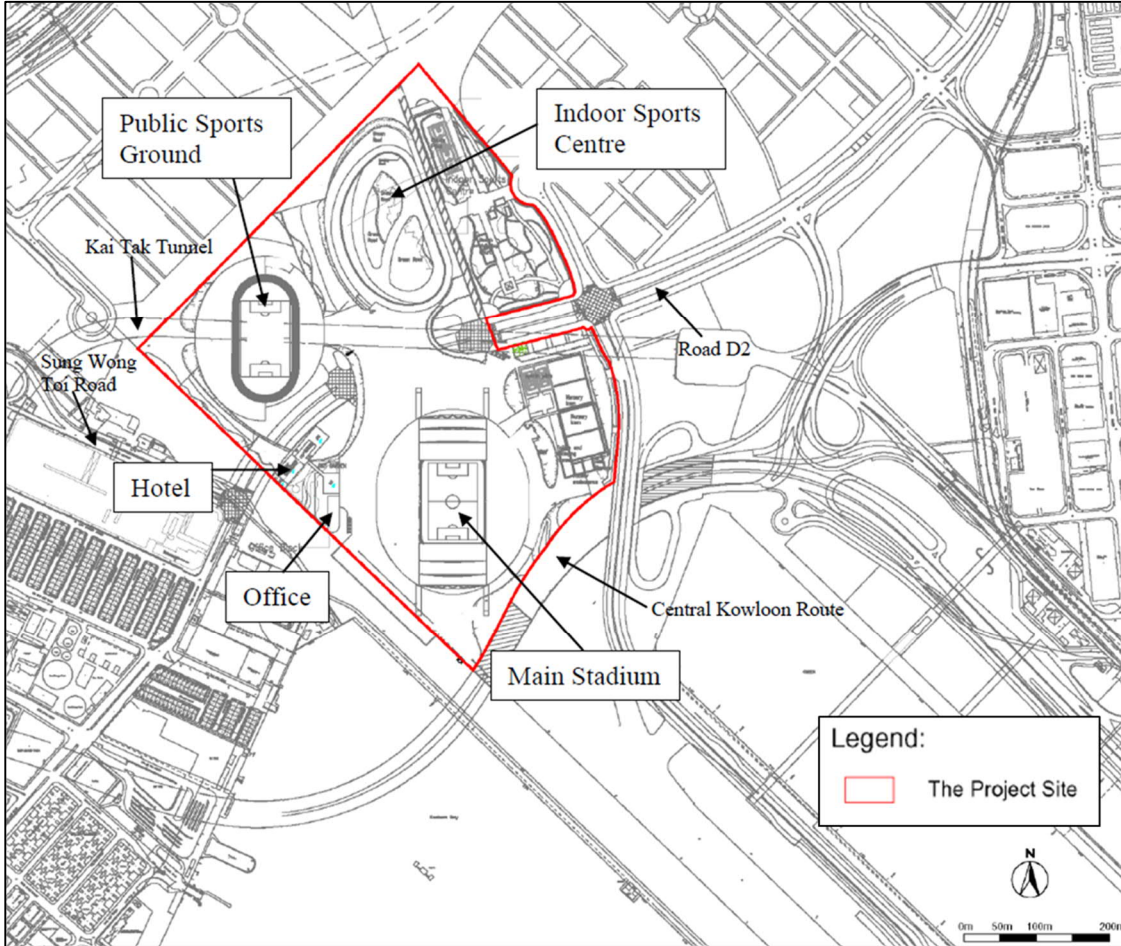

## Appendix C. Construction Programme



## Appendix D. Event and Action Plan

Should non-compliance of the air quality criteria occur, actions in accordance with the Event and Action Plan in **Table D.1** and **Table D.2** shall be carried out.

**Table D.1: Event and Action Plan for Construction Air Quality (Action Level)**

Event	Action			
	ET	IEC	SOR	Contracted Party
<b>Action Level</b>				
Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Inform IEC, SOR and Contracted Party;</li> <li>2. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>3. Repeat measurement to confirm finding.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contracted Party's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contracted Party.</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Inform IEC, SOR and Contracted Party;</li> <li>2. Identify source;</li> <li>3. Advise the SOR on the effectiveness of the proposed remedial measures;</li> <li>4. Repeat measurements to confirm findings;</li> <li>5. Increase monitoring frequency to daily;</li> <li>6. Discuss with IEC, SOR and Contracted Party on remedial actions required;</li> <li>7. If exceedance continues, arrange meeting with IEC and SOR;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contracted Party's working method;</li> <li>3. Discuss with ET and Contracted Party on possible remedial measures;</li> <li>4. Advise the ET/SOR on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise Implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contracted Party;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit proposals for remedial to SOR and IEC within 3 working days of notification;</li> <li>2. Implement the agreed proposals;</li> <li>3. Amend proposal if appropriate.</li> </ol>

**Table D.2: Event and Action Plan for Construction Air Quality (Limit Level)**

Event	Action			
	ET	IEC	ET	Contracted Party
<b>Limit Level</b>				
Exceedance for one sample	1. Inform IEC, SOR, Contracted Party and EPD; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss with ET and Contracted Party on possible remedial measures; 4. Advise the SOR on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Amend proposal if appropriate.
Exceedance for two or more consecutive samples	1. Notify IEC, SOR, Contracted Party and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and SOR and Contracted Party to discuss the remedial actions to be taken; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 4. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 5. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. In consultation with the IEC, agree with the Contracted Party on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases.	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to SOR and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the SOR until the exceedance ceases.

Should non-compliance of the noise criteria occur, actions in accordance with the Event and Action Plan in **Table D.3** shall be carried out.

**Table D.3: Event and Action Plan for Construction Noise**

Event	Action			
	ET	IEC	ET	Contracted Party
<b>Action Level</b>	1. Notify IEC, SOR and Contracted Party of exceedance; 2. Identify source; 3. Investigate the causes of exceedance and propose remedial measures; 4. Report the results of investigation to the IEC, SOR and Contracted Party; 5. Discuss with the IEC, SOR and Contracted Party and formulate remedial measures; 6. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contracted Party and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented	1. Submit noise mitigation proposals to SOR with copy to ET and IEC; 2. Implement noise mitigation proposals.
<b>Limit Level</b>	1. Inform IEC, SOR, EPD and Contracted Party; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, SOR and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 2. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented; 5. If exceedance continues, investigate what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to SOR with copy to ET and IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Terminate the relevant portion of works as determined by the SOR until the exceedance ceases.

# Appendix E. Environmental Site Inspection and Monitoring Schedule

**Table E.1: Site Inspection and Monitoring Schedule for October 2020**

Impact Environmental Monitoring Schedule for October 2020

Sun	Mon	Tue	Wed	Thu	Fri	Sat
				1 National Day	2 The day after the mid-Autumn Festival	3 AMS1 AMS2
4	5	6	7 site inspection landscape and visual audit	8	9 AMS1, NMS1 AMS2, NMS2	10
11	12	13	14 site inspection	15 AMS1, NMS1 AMS2, NMS2	16	17
18	19	20 site inspection landscape and visual audit	21 AMS1, NMS1 AMS2, NMS2	22	23	24
25	26 Chung Yeung Festival	27 AMS1, NMS1 AMS2, NMS2	28 site inspection	29	30	31

 Air Quality/Noise Monitoring

Remark: Joint site walk with IEC on 20 and 28 October 2020

**Table E.2: Tentative Site Inspection and Monitoring Schedule for November 2020**

**Tentative Impact Environmental Monitoring Schedule for November 2020**

Sun	Mon	Tue	Wed	Thu	Fri	Sat
1	2	3	4	5	6	7
	AMS1, NMS1 AMS2, NMS2		site inspection		AMS1 AMS2	
8	9	10	11	12	13	14
			site inspection landscape and visual audit	AMS1, NMS1 AMS2, NMS2		
15	16	17	18	19	20	21
			AMS1, NMS1 AMS2, NMS2 site inspection			
22	23	24	25	26	27	28
		AMS1, NMS1 AMS2, NMS2	site inspection landscape and visual audit			
29	30					
	AMS1, NMS1 AMS2, NMS2					

 Air Quality/Noise Monitoring

Remark: The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)



## Appendix F. Calibration Certificates



## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN

WORK ORDER : **HK1950891**

CLIENT : ENVIROTECH SERVICES CO.

ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD,  
TUEN MUN, N.T. HONG KONG

SUB-BATCH : 1

DATE RECEIVED : 3-DEC-2019

DATE OF ISSUE : 13-DEC-2019

PROJECT : ---

NO. OF SAMPLES : 1

CLIENT ORDER : ---

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc., if any) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1950891  
SUB-BATCH : 1  
CLIENT : ENVIROTECH SERVICES CO.  
PROJECT : ---



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1950891-001	S/N: 627784	Equipments	03-Dec-2019	627784

# Equipment Verification Report (TSP)

## Equipment Calibrated:

Type: Laser Dust monitor  
 Manufacturer: Sibata LD-3B  
 Serial No. 6Z7784  
 Equipment Ref: Nil  
 Job Order HK1950891

## Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
 Location & Location ID: AUES office (calibration room)  
 Equipment Ref: HVS 018  
 Last Calibration Date: 3 December 2019

## Equipment Verification Results:

Verification Date: 10 December 2019


Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr02min	09:08 ~ 11:10	18.4	1018.6	0.032	3020	24.8
2hr01min	11:15 ~ 13:16	18.4	1018.6	0.044	3185	26.4
2hr01min	13:22 ~ 15:23	18.4	1018.6	0.050	4141	34.3

### Linear Regression of Y or X

Slope (K-factor): 0.0015

Correlation Coefficient 0.9833

Date of Issue 13 December 2019

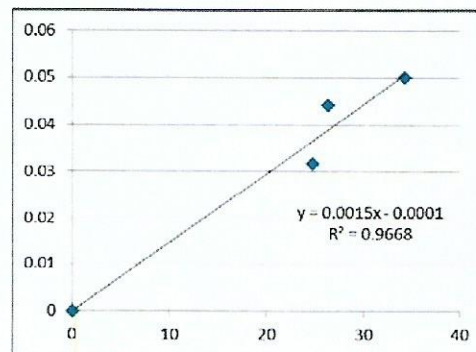

### Remarks:

1. **Strong Correlation (R>0.8)**
  2. Factor 0.0015 should be applied for TSP monitoring
- \*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : *Fai So* Date : 13 December 2019

QC Reviewer : Ben Tam Signature : *Ben Tam* Date : 13 December 2019



### SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN  
CLIENT : ENVIROTECH SERVICES CO.  
ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD,  
TUEN MUN, N.T. HONG KONG  
PROJECT : ----

WORK ORDER : **HK1950885**  
SUB-BATCH : 1  
DATE RECEIVED : 3-DEC-2019  
DATE OF ISSUE : 13-DEC-2019  
NO. OF SAMPLES : 1  
CLIENT ORDER : ----

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc., if any) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1950885  
SUB-BATCH : 1  
CLIENT : ENVIROTECH SERVICES CO.  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1950885-001	S/N: 235780	Equipments	03-Dec-2019	235780

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 235780  
Equipment Ref: Nil  
Job Order HK1950885

### Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 3 December 2019


### Equipment Verification Results:

Verification Date: 10 December 2019

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr02min	09:08 ~ 11:10	18.4	1018.6	0.032	2989	24.5
2hr01min	11:15 ~ 13:16	18.4	1018.6	0.044	3203	26.6
2hr01min	13:22 ~ 15:23	18.4	1018.6	0.050	4060	33.7

### Linear Regression of Y or X

Slope (K-factor): 0.0015  
Correlation Coefficient 0.9855  
Date of Issue 13 December 2019

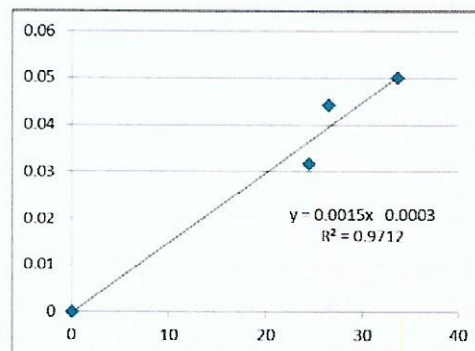

### Remarks:

1. Strong Correlation ( $R > 0.8$ )
2. Factor 0.0015 should be applied for TSP monitoring

\*If  $R < 0.5$ , repair or re-verification is required for the equipment

Operator: Fai So Signature:  Date: 13 December 2019

QC Reviewer: Ben Tam Signature:  Date: 13 December 2019



# Certificate of Calibration 校正證書

Certificate No. : C196453  
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC19-2418)      Date of Receipt / 收件日期 : 18 November 2019

Description / 儀器名稱 : Precision Acoustic Calibrator  
Manufacturer / 製造商 : LARSON DAVIS  
Model No. / 型號 : CAL200  
Serial No. / 編號 : 11334  
Supplied By / 委託者 : Envirotech Services Co.  
Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,  
New Territories, Hong Kong

## TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$   
Line Voltage / 電壓 : ---

## TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 30 November 2019

## TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification & user's specified acceptance criteria.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By :   
測試 : \_\_\_\_\_  
H T Wong  
Technical Officer

Certified By :   
核證 : \_\_\_\_\_  
K C Lee  
Engineer

Date of Issue : 3 December 2019  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。





# Certificate of Calibration

## 校正證書

Certificate No. : C196453  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C193756
CL281	Multifunction Acoustic Calibrator	CDK1806821
TST150A	Measuring Amplifier	C181288

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	User's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.8	± 0.5	± 0.2
114 dB, 1 kHz	113.7		

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1

Remarks : - The user's specified acceptance criteria (user's spec.) is a customer pre-defined operating tolerance of the UUT, suitable for one's own intended use.

- The uncertainties are for a confidence probability of not less than 95 %.


### Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration 校正證書

Certificate No. : C203822  
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC20-1389)

Date of Receipt / 收件日期 : 30 June 2020

Description / 儀器名稱 : Sound Level Meter

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 01010406

Supplied By / 委託者 : Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,  
New Territories, Hong Kong

## TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

## TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 9 July 2020

## TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.


The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested By  
測試

  
K P Cheuk  
Assistant Engineer

Certified By  
核證

  
K C Lee  
Engineer

Date of Issue  
簽發日期

10 July 2020

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C203822

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C200258
CL281	Multifunction Acoustic Calibrator	CDK1806821

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.8	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.8 (Ref.)
				104.00		103.9
				114.00		113.8

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.8	Ref.
			Slow			93.8	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C203822

證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.5	-26.2 ± 1.5
					125 Hz	77.6	-16.1 ± 1.5
					250 Hz	85.1	-8.6 ± 1.4
					500 Hz	90.6	-3.2 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	95.1	+1.2 ± 1.6
					4 kHz	94.9	+1.0 ± 1.6
					8 kHz	92.8	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.4	-4.3 (+3.0 ; -6.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	92.9	-0.8 ± 1.5
					125 Hz	93.6	-0.2 ± 1.5
					250 Hz	93.8	0.0 ± 1.4
					500 Hz	93.8	0.0 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	93.7	-0.2 ± 1.6
					4 kHz	93.0	-0.8 ± 1.6
					8 kHz	90.9	-3.0 (+2.1 ; -3.1)
					12.5 kHz	87.5	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C203822  
證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 04871

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.


本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

## **Appendix G. Monitoring Data and Graphical Plots (Air Quality and Noise)**

## Data for 1-hour TSP Monitoring at Station AMS1

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )
03-Oct-20	8:57	9:57	Sunny	5.0	88	62
03-Oct-20	9:57	10:57	Sunny	4.4	80	72
03-Oct-20	10:57	11:57	Sunny	4.2	108	79
09-Oct-20	9:03	10:03	Sunny	2.8	21	65
09-Oct-20	10:03	11:03	Sunny	2.5	43	71
09-Oct-20	11:03	12:03	Sunny	2.8	3	77
15-Oct-20	10:02	11:02	Fine	4.7	58	30
15-Oct-20	11:02	12:02	Fine	6.1	99	42
15-Oct-20	12:02	13:02	Fine	6.9	97	49
21-Oct-20	9:06	10:06	Sunny	3.9	340	55
21-Oct-20	10:06	11:06	Sunny	3.9	326	44
21-Oct-20	11:06	12:06	Sunny	5.3	300	46
27-Oct-20	9:07	10:07	Sunny	3.3	113	64
27-Oct-20	10:07	11:07	Sunny	6.1	98	59
27-Oct-20	11:07	12:07	Sunny	4.4	105	54


## Graphical Presentation for 1-hour TSP Monitoring at AMS1

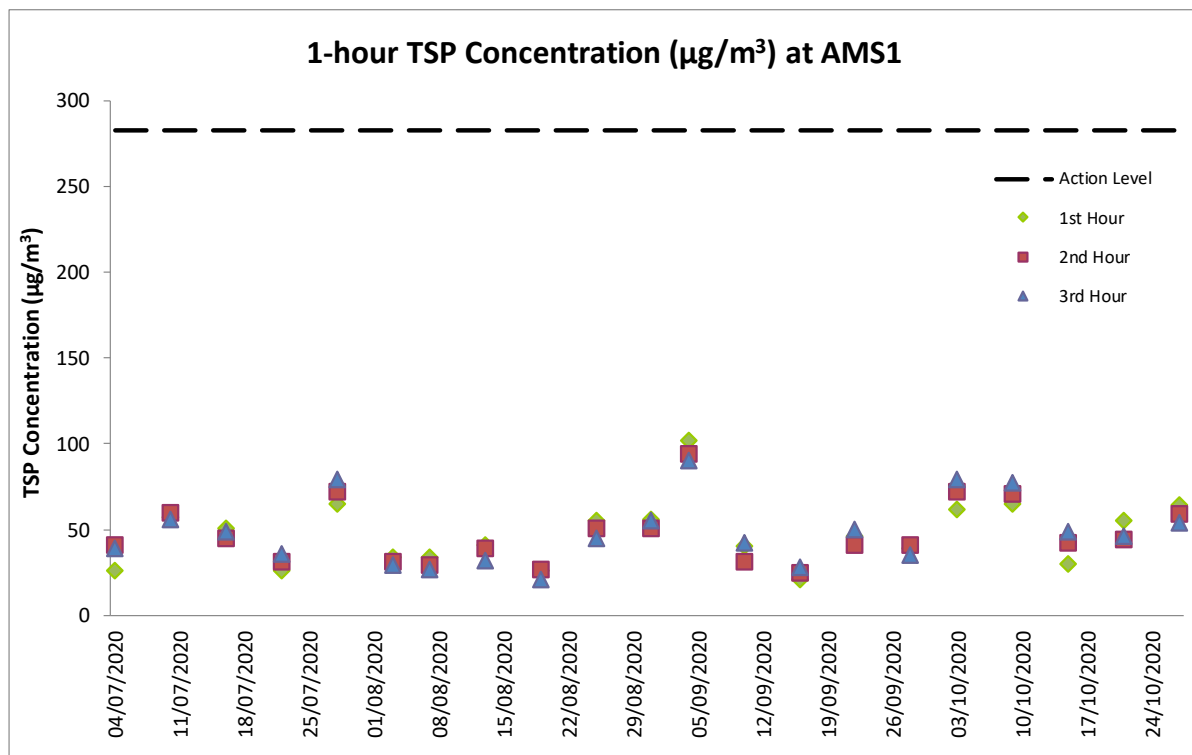

## Data for 1-hour TSP Monitoring at Station AMS2

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )
03-Oct-20	8:45	9:45	Sunny	4.2	78	74
03-Oct-20	9:45	10:45	Sunny	5.3	87	69
03-Oct-20	10:45	11:45	Sunny	4.4	47	76
09-Oct-20	8:18	9:18	Sunny	1.7	346	63
09-Oct-20	9:18	10:18	Sunny	2.8	352	69
09-Oct-20	10:18	11:18	Sunny	2.8	3	75
15-Oct-20	9:02	10:02	Cloudy	5.8	83	39
15-Oct-20	10:02	11:02	Cloudy	4.7	58	46
15-Oct-20	11:02	12:02	Cloudy	6.1	99	40
21-Oct-20	8:22	9:22	Sunny	4.7	351	60
21-Oct-20	9:22	10:22	Sunny	3.1	335	47
21-Oct-20	10:22	11:22	Sunny	5.0	304	50
27-Oct-20	8:20	9:20	Sunny	3.1	87	66
27-Oct-20	9:20	10:20	Sunny	4.2	102	54
27-Oct-20	10:20	11:20	Sunny	6.1	94	70

## Graphical Presentation for 1-hour TSP Monitoring at AMS2

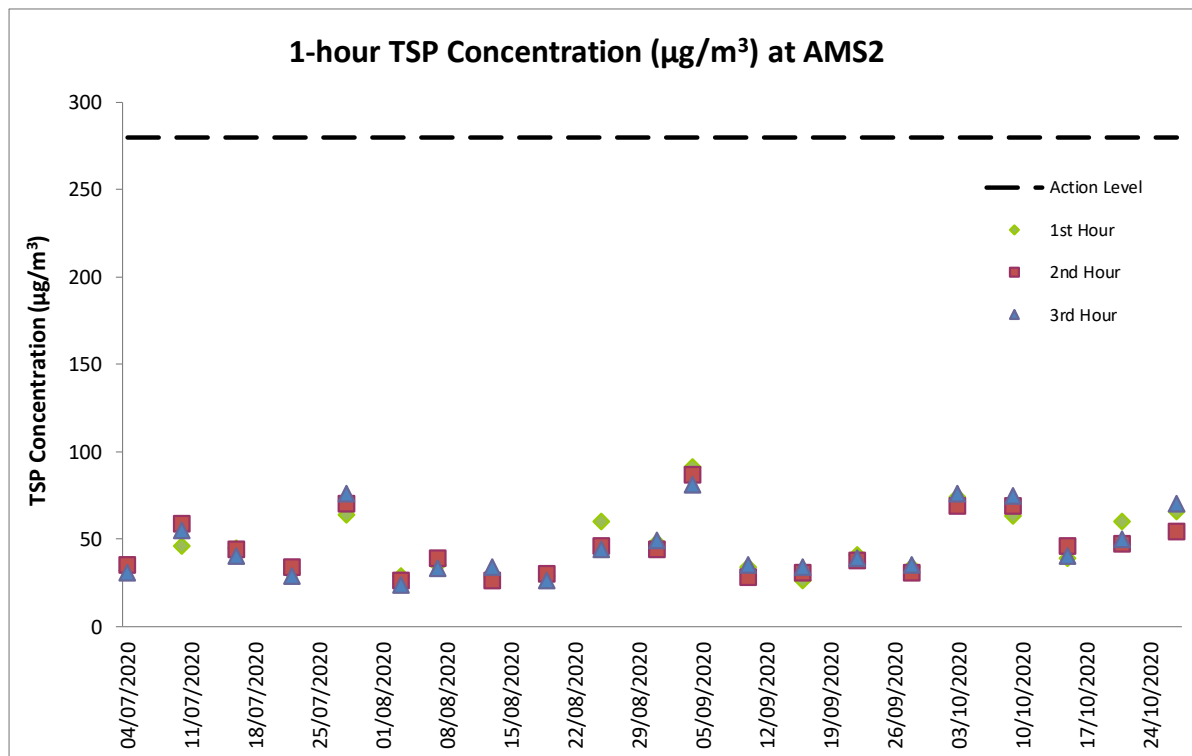




### Data for Noise Monitoring at Station NMS1

Date	Time	Weather	L <sub>eq</sub> (5min)	L <sub>10</sub>	L <sub>90</sub>	Measured L <sub>eq</sub> (30min)
09-Oct-20	09:05	Sunny	68.9	70.9	65.8	70.6
09-Oct-20	09:10	Sunny	70.1	72.4	66.1	
09-Oct-20	09:15	Sunny	70.2	72.3	66.4	
09-Oct-20	09:20	Sunny	71.1	73.5	67.0	
09-Oct-20	09:25	Sunny	70.9	72.6	66.8	
09-Oct-20	09:30	Sunny	72.0	74.7	67.9	
15-Oct-20	10:04	Fine	72.6	74.4	69.4	72.5
15-Oct-20	10:09	Fine	72.9	74.4	70.7	
15-Oct-20	10:14	Fine	72.7	74.5	70.5	
15-Oct-20	10:19	Fine	71.7	73.6	69.7	
15-Oct-20	10:24	Fine	72.9	74.6	70.6	
15-Oct-20	10:29	Fine	71.8	73.9	70.0	
21-Oct-20	09:08	Sunny	68.7	70.8	65.1	68.9
21-Oct-20	09:13	Sunny	67.9	69.5	64.9	
21-Oct-20	09:18	Sunny	69.4	71.2	65.3	
21-Oct-20	09:23	Sunny	69.4	71.3	65.4	
21-Oct-20	09:28	Sunny	68.3	70.1	65.2	
21-Oct-20	09:33	Sunny	69.6	71.5	66.0	
27-Oct-20	09:09	Sunny	68.7	70.9	65.1	70.1
27-Oct-20	09:14	Sunny	69.1	71.2	66.9	
27-Oct-20	09:19	Sunny	70.1	72.3	67.1	
27-Oct-20	09:24	Sunny	70.9	72.4	67.5	
27-Oct-20	09:29	Sunny	71.1	73.5	67.9	
27-Oct-20	09:34	Sunny	69.9	71.6	66.9	


### Graphical Presentation for Noise Monitoring at NMS1

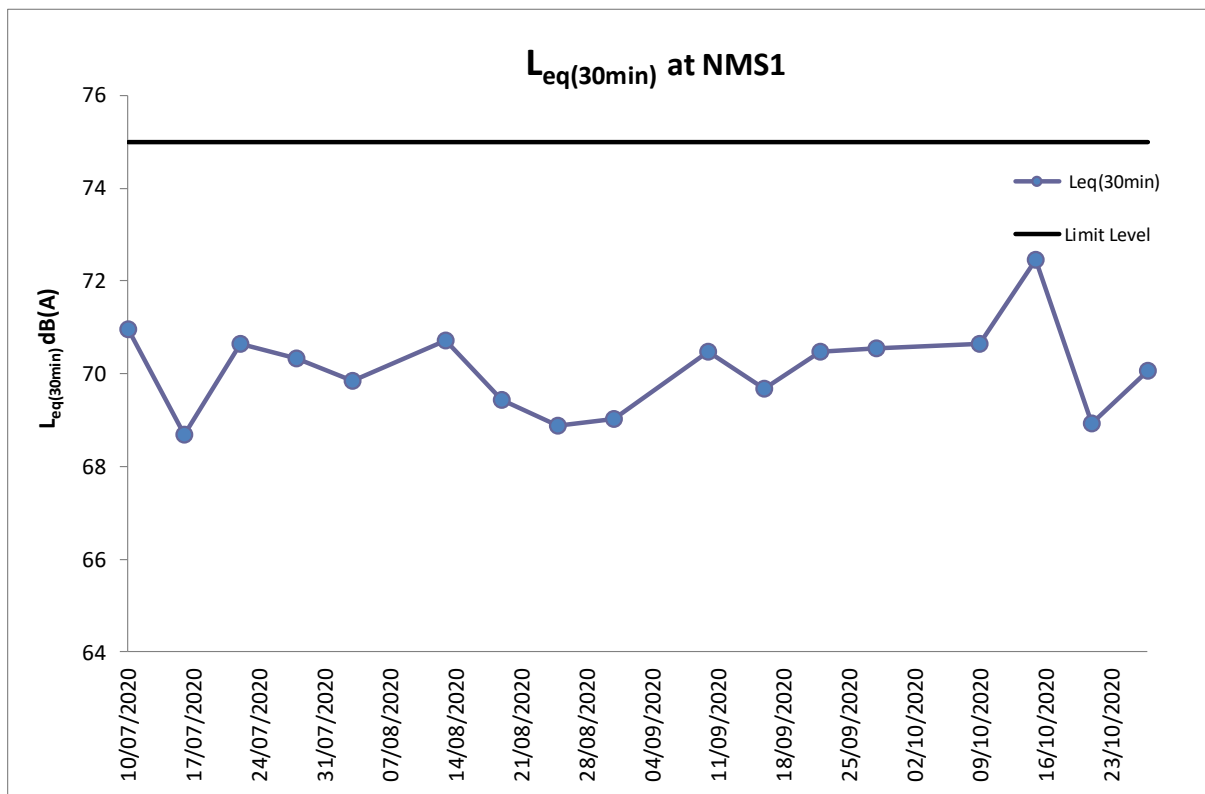

## Data for Noise Monitoring at Station NMS2



Date	Time	Weather	L <sub>eq</sub> (5min)	L <sub>10</sub>	L <sub>90</sub>	Measured L <sub>eq</sub> (30min)
09-Oct-20	08:20	Sunny	68.1	70.1	65.1	69.7
09-Oct-20	08:25	Sunny	69.0	71.4	66.2	
09-Oct-20	08:30	Sunny	69.4	71.5	66.6	
09-Oct-20	08:35	Sunny	70.1	72.3	67.0	
09-Oct-20	08:40	Sunny	71.1	73.0	67.7	
09-Oct-20	08:45	Sunny	69.9	71.5	66.8	
15-Oct-20	09:14	Cloudy	70.4	72.8	67.2	69.9
15-Oct-20	09:19	Cloudy	69.6	71.6	67.0	
15-Oct-20	09:24	Cloudy	70.4	72.5	66.8	
15-Oct-20	09:29	Cloudy	69.8	71.9	66.5	
15-Oct-20	09:34	Cloudy	69.4	71.7	66.2	
15-Oct-20	09:39	Cloudy	69.9	72.1	66.9	
21-Oct-20	08:24	Sunny	68.2	70.1	65.3	68.8
21-Oct-20	08:29	Sunny	67.1	69.8	64.7	
21-Oct-20	08:34	Sunny	69.1	71.5	66.6	
21-Oct-20	08:39	Sunny	70.1	72.4	67.3	
21-Oct-20	08:44	Sunny	69.2	71.3	66.1	
21-Oct-20	08:49	Sunny	68.7	70.6	65.9	
27-Oct-20	08:25	Sunny	68.0	70.1	65.1	68.4
27-Oct-20	08:30	Sunny	67.1	69.5	64.9	
27-Oct-20	08:35	Sunny	67.9	69.8	64.7	
27-Oct-20	08:40	Sunny	68.4	70.3	65.9	
27-Oct-20	08:45	Sunny	69.1	71.2	65.2	
27-Oct-20	08:50	Sunny	69.7	71.6	65.8	

### Graphical Presentation for Noise Monitoring at NMS2


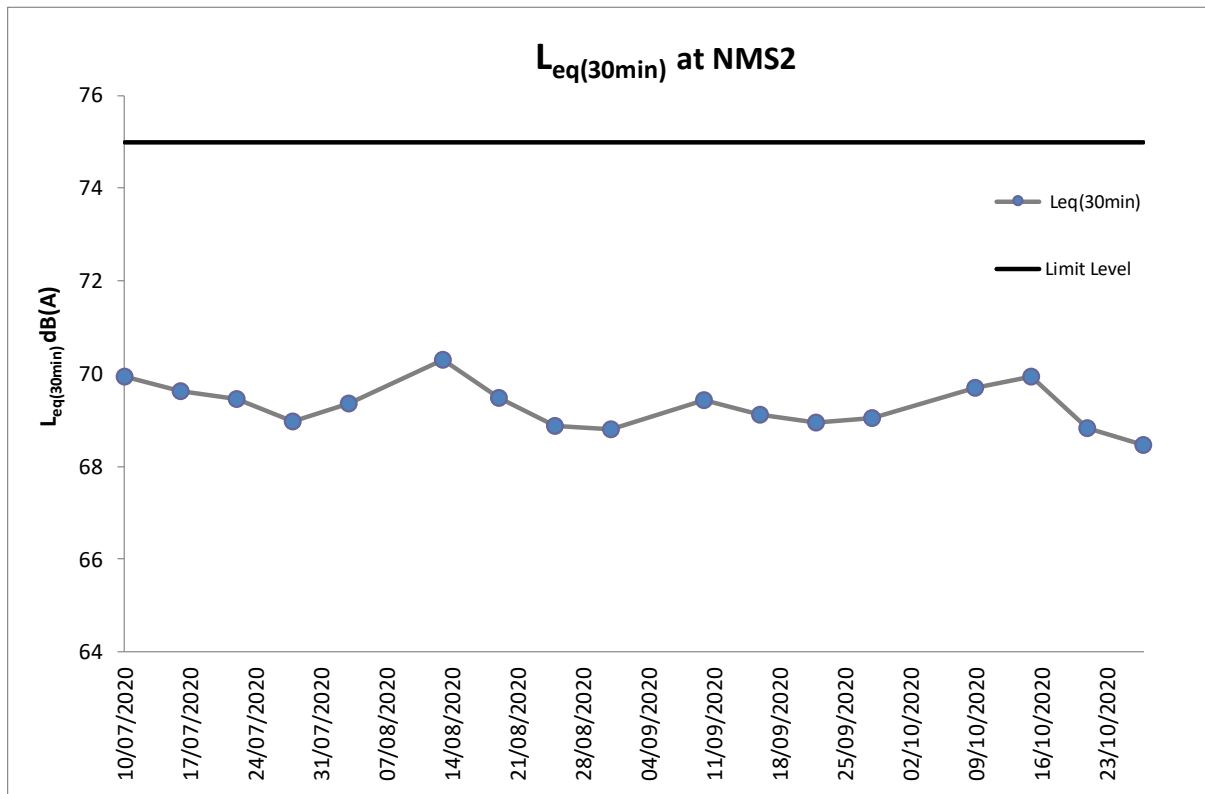


## Appendix H. Wind Data



3 October 2020

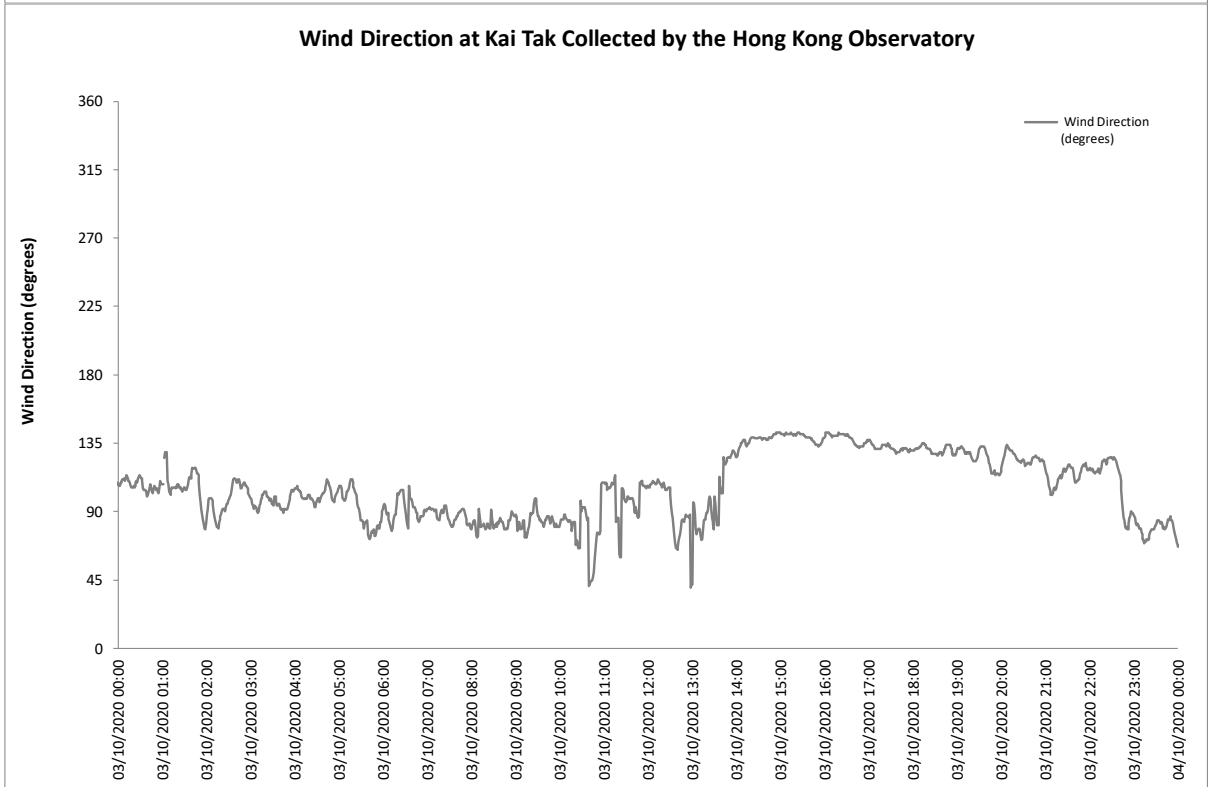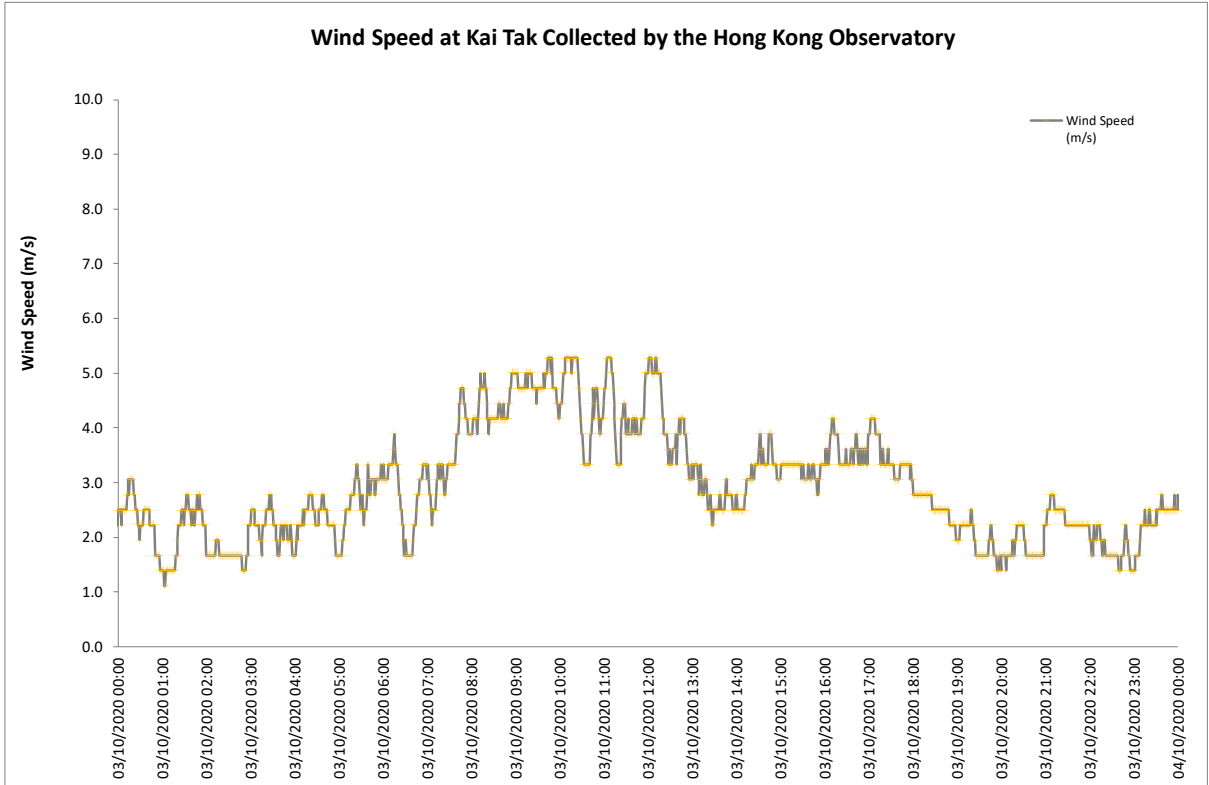

9 October 2020

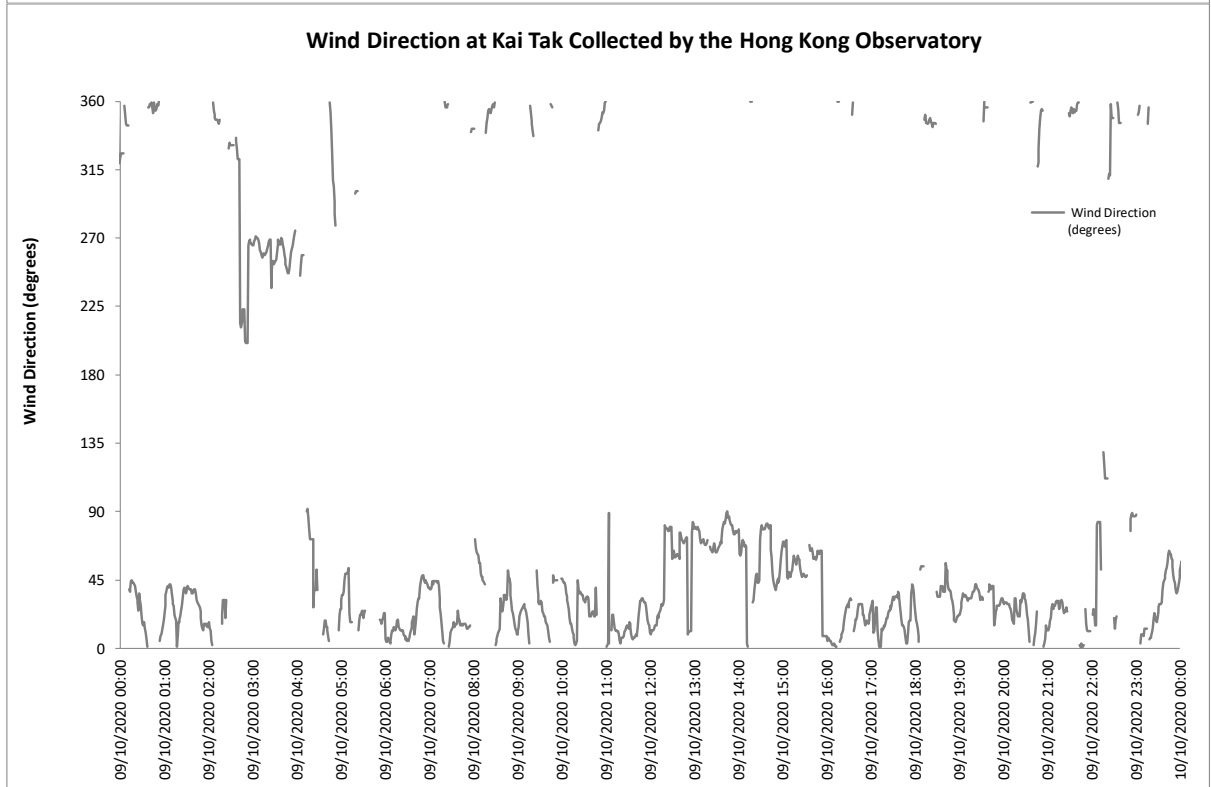
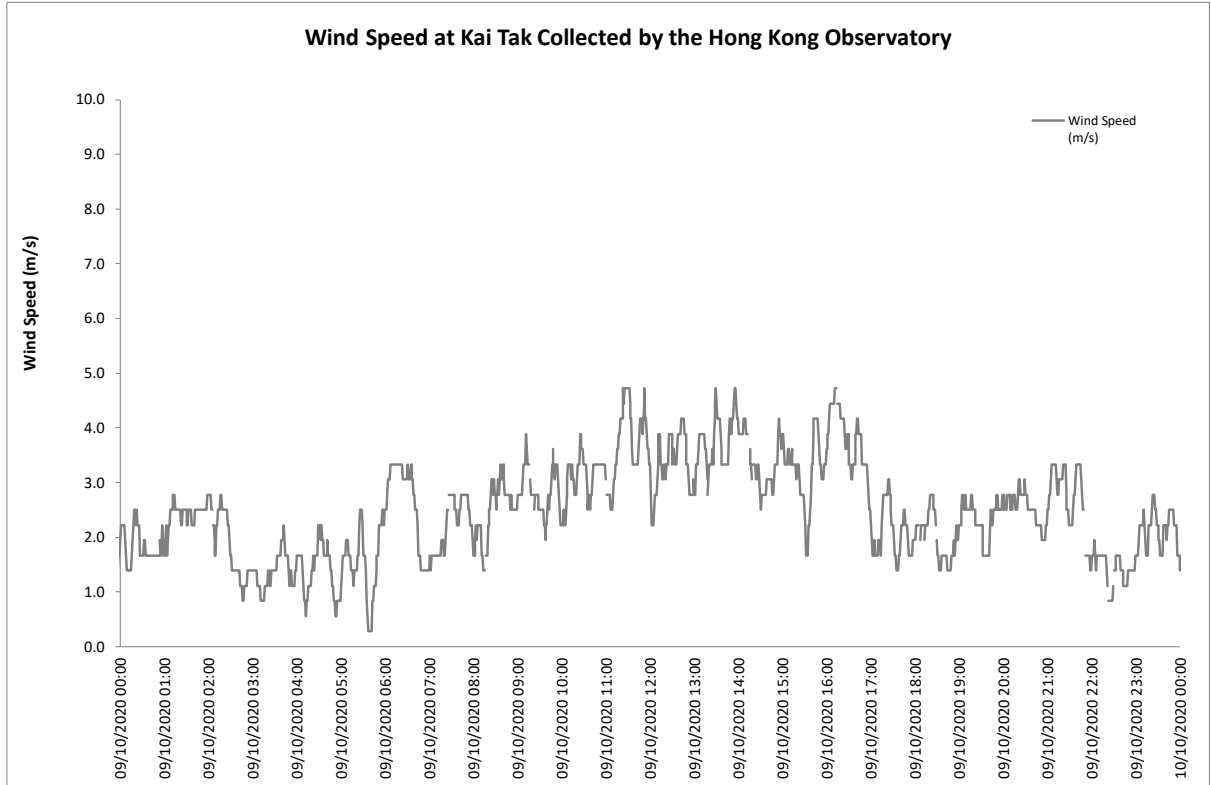


15 October 2020

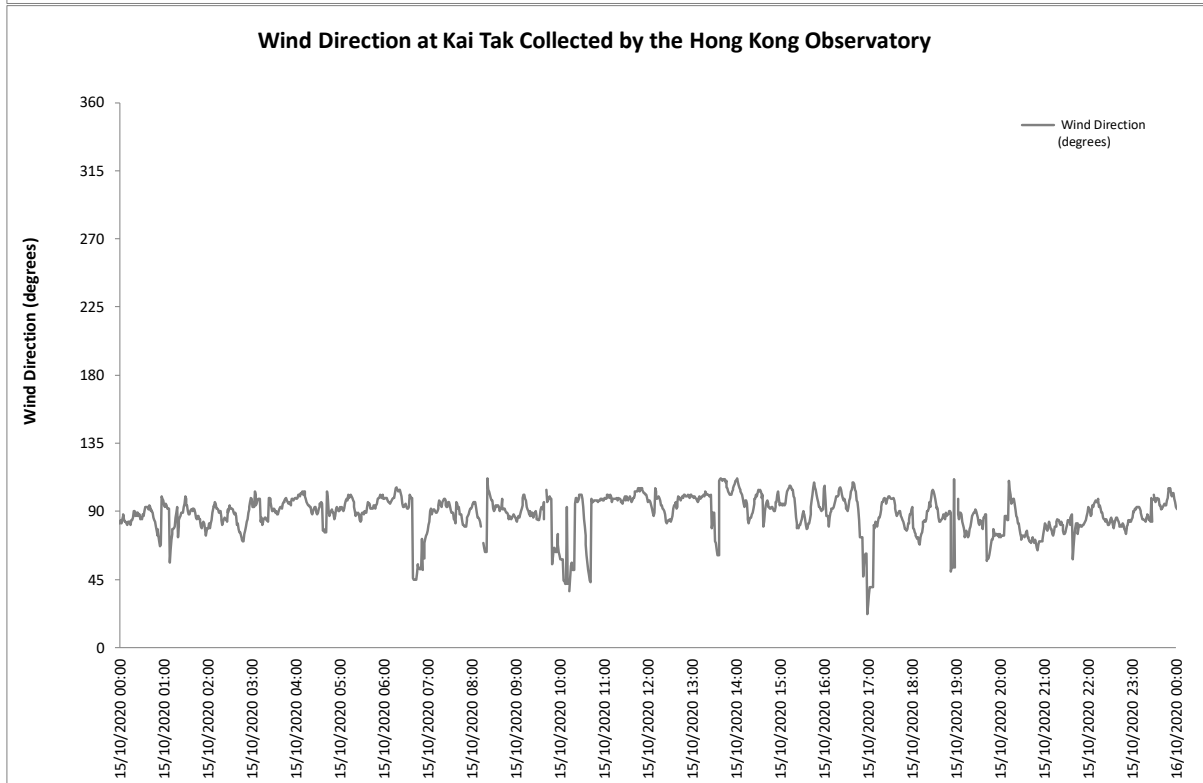
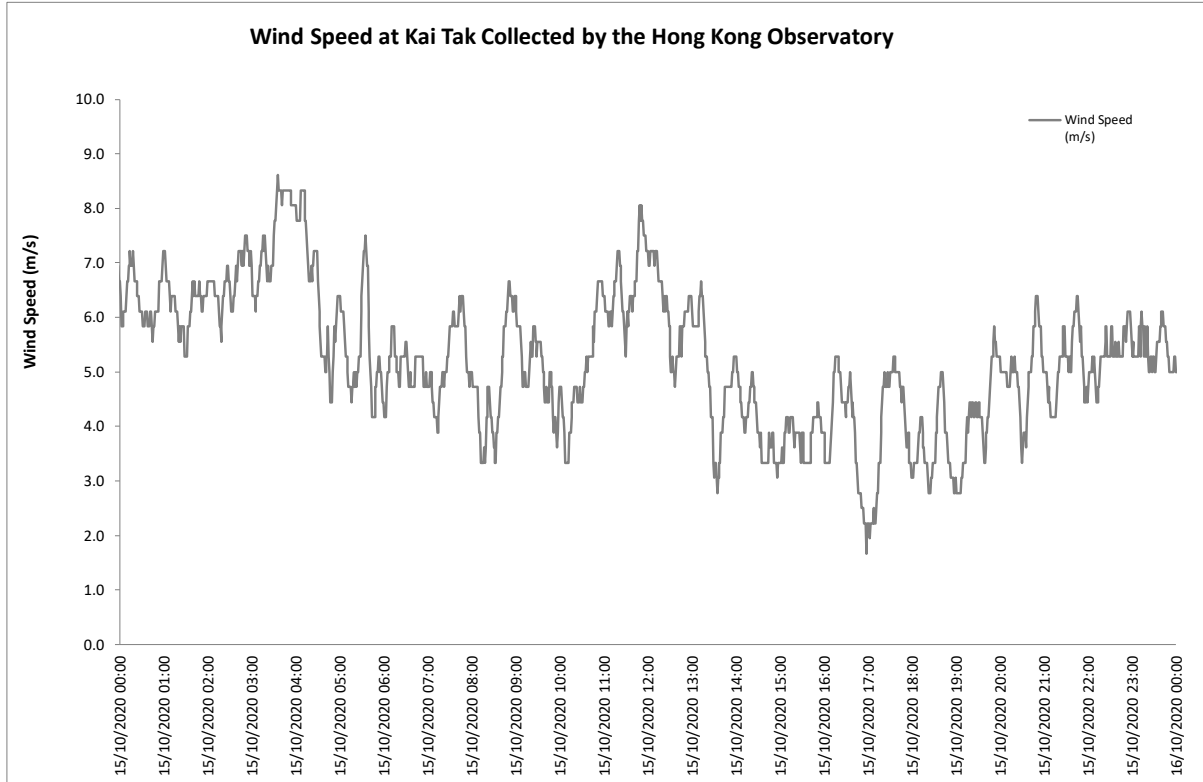




21 October 2020

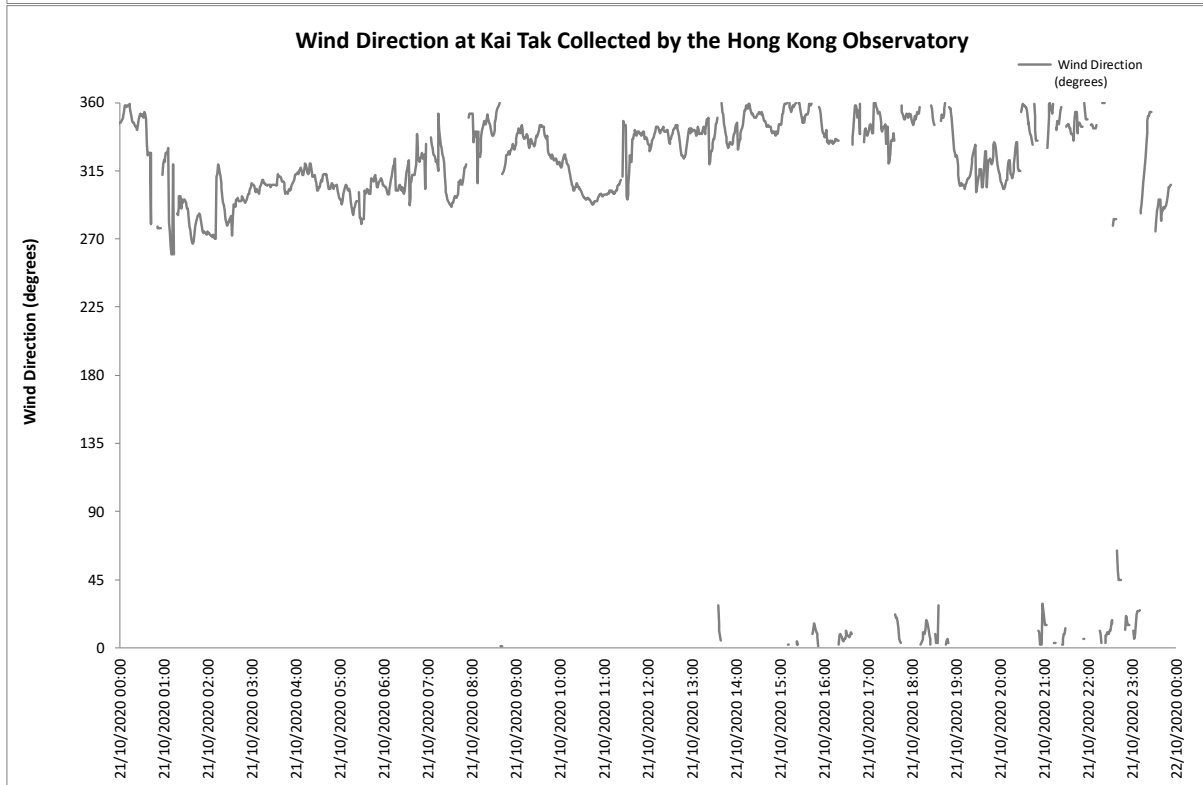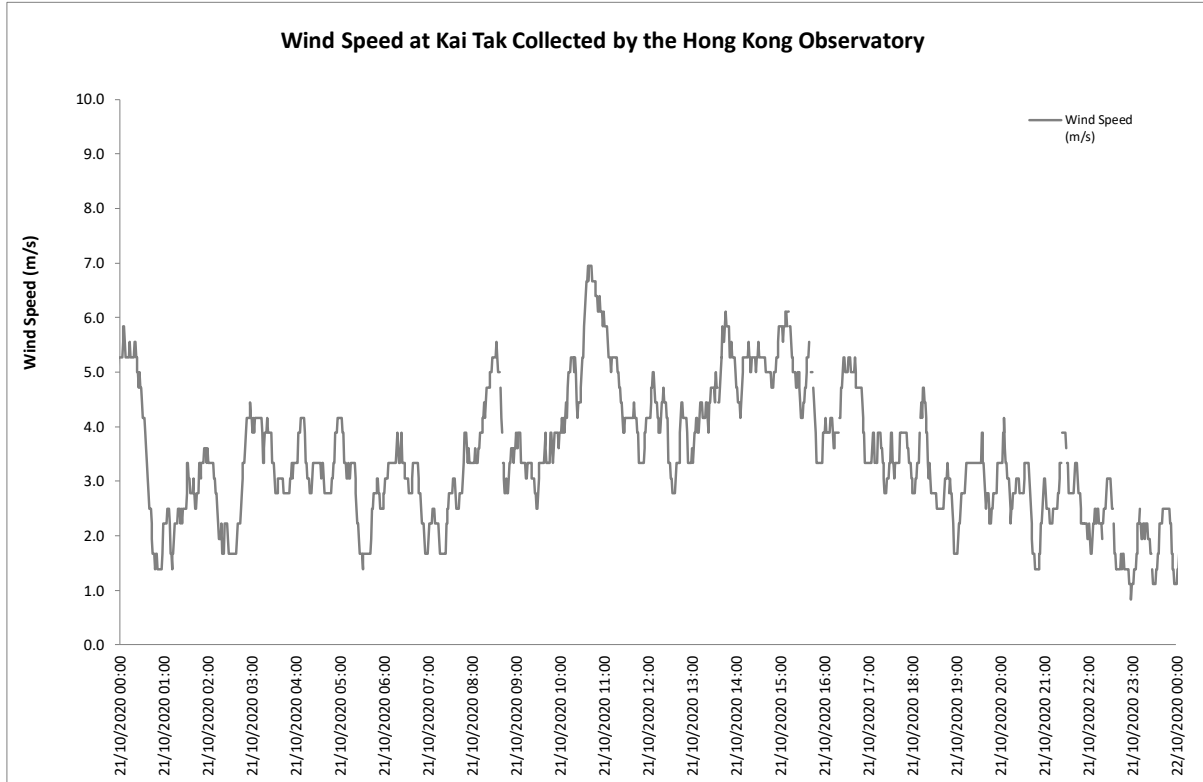

27 October 2020

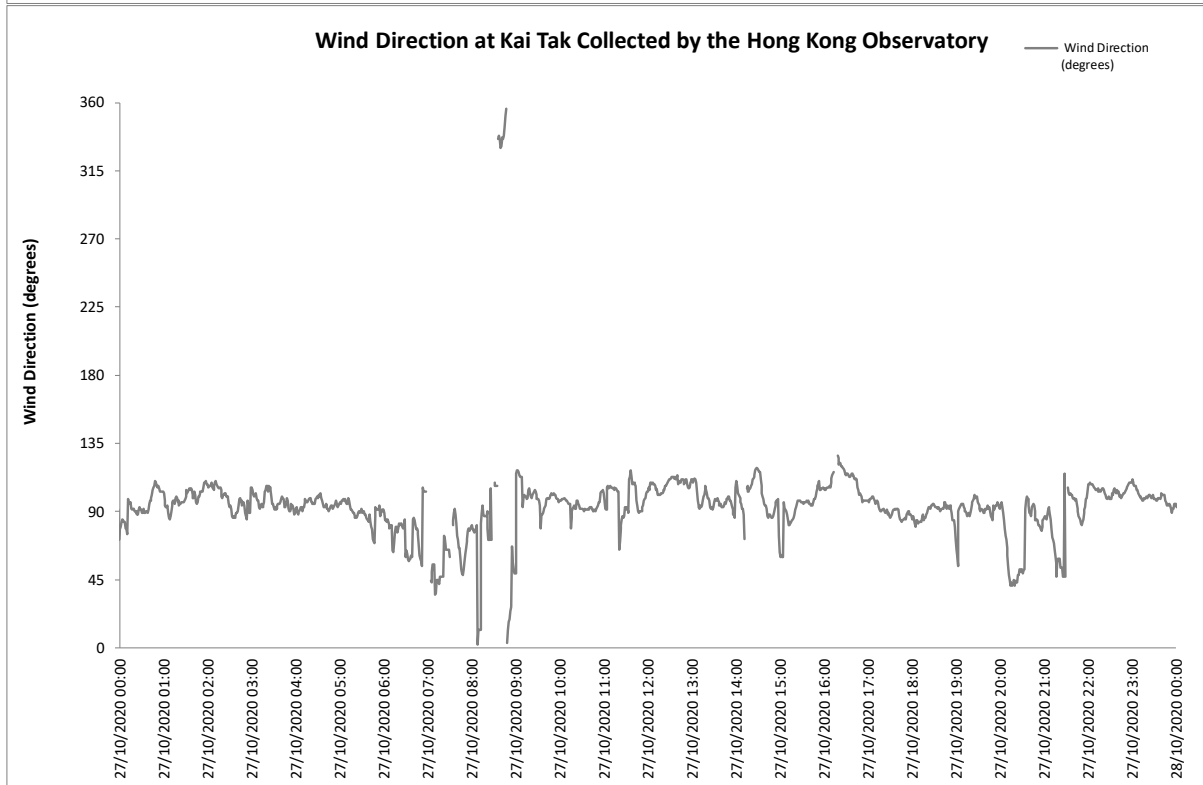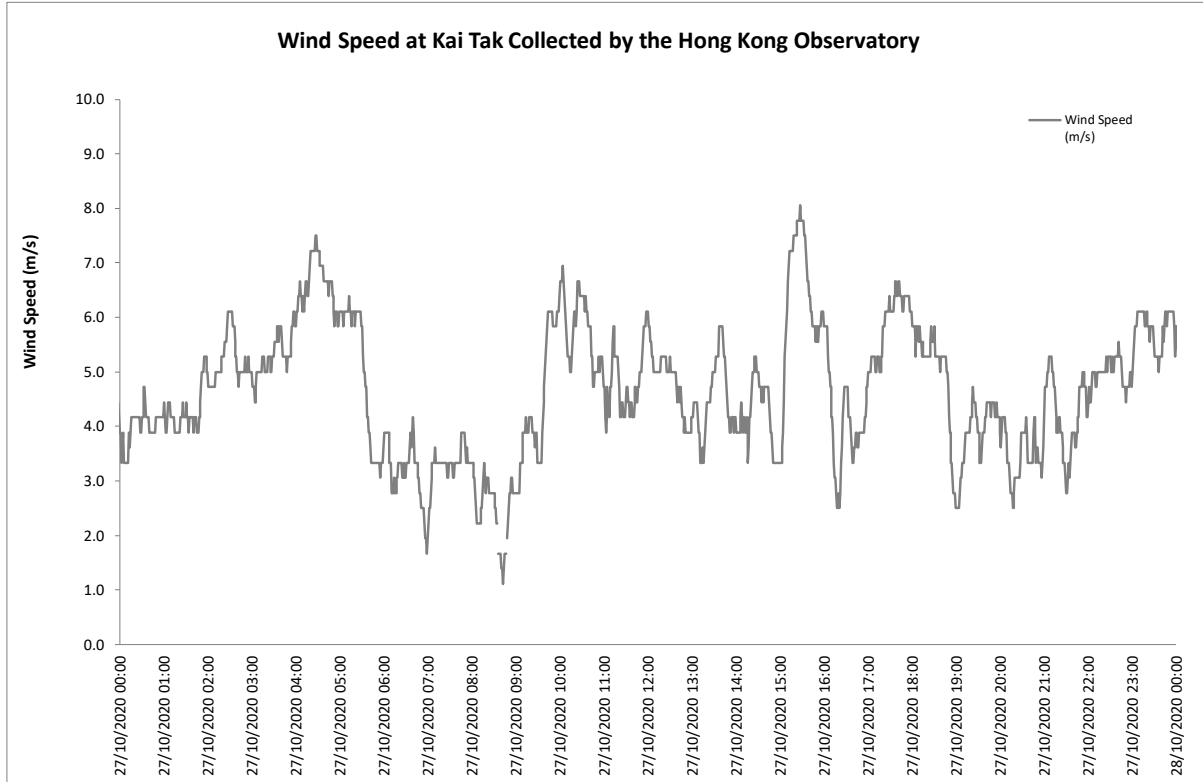

## Appendix I. Waste Flow Table

Project: Kai Tak Sport Park  
 Contract No.: HAB/ KTSP/ 01  
 Contract Title: Design, Construction and Operation of the Kai Tak Sports Park at Kai Tak, Kowloon City District, Hong Kong  
 Year of Record: 2019-2020

### Monthly Waste Flow Table

Month	Total Quantity Generated	Total Quantity Generated (Excluded Excavated Material)	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Materials Generated Monthly						Remarks
			Excavated Materials			Non-excavated Materials					Metals (steel bar / metal strip) <sup>(1)</sup>	Metals (aluminum can) <sup>(1)</sup>	Paper / cardboard packaging <sup>(1)</sup>	Plastics <sup>(1) &amp; (4)</sup>	Chemical waste (wasted lubricant oil/ oil container)	Other, e.g. general refuse	
			Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities							
(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)		
	a1	a2	b	b	b	c	d	e	f	g	h	i	j	k	l	m	
Jan-19																	
Feb-19	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Mar-19	4960.89	4741.39	219.50	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.84	0.00	0.00	0.00	0.00	4729.55	
Apr-19	1218.47	1211.81	6.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.06	0.00	1211.75	
May-19	87.29	87.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01	0.00	87.28	
Jun-19	80.77	80.77	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.67	0.00	0.08	0.42	0.00	79.61	
Jul-19	2302.12	614.75	1687.37	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.26	0.95	0.00	613.54	
Aug-19	3619.81	280.59	3339.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.77	0.00	0.00	1.29	0.60	276.93	
Sep-19	9840.53	350.02	9490.51	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.41	0.60	348.01	
Oct-19	11504.49	543.12	10961.37	0.00	0.00	0.00	0.00	0.00	0.00	0.00	81.95	0.00	1.43	0.58	0.00	459.16	
Nov-19	4717.41	313.12	4404.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00	69.84	0.00	0.00	0.89	0.00	242.39	
Dec-19	5185.04	102.38	5082.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.53	0.80	100.05	
Jan-20	12105.75	125.72	11980.03	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.32	0.00	0.57	0.03	0.00	108.80	
Feb-20	18104.46	100.08	13459.32	0.00	4545.06	0.00	0.00	0.00	0.00	0.00	23.64	0.00	0.00	0.46	0.00	75.98	
Mar-20	35699.68	236.48	6615.03	0.00	28848.17	0.00	0.00	0.00	0.00	0.00	90.73	0.00	0.50	1.82	0.80	142.63	
Apr-20	42585.99	136.86	0.00	0.00	42449.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.06	0.00	136.80	
May-20	64505.99	218.37	0.00	0.00	64287.62	0.00	0.00	0.00	0.00	0.00	47.41	0.00	0.40	1.09	0.00	169.47	
Jun-20	44982.44	336.11	6519.25	0.00	38127.08	0.00	0.00	0.00	0.00	0.00	171.56	0.00	0.58	1.46	0.80	161.71	
Jul-20	43467.27	601.19	0.00	0.00	42866.08	0.00	0.00	0.00	0.00	0.00	377.41	0.00	0.49	1.01	0.00	222.28	
Aug-20	61579.38	1092.15	3771.32	0.00	56715.91	0.00	0.00	0.00	0.00	0.00	834.10	0.00	0.69	1.15	0.00	256.21	
Sep-20	111046.04	730.59	0.00	0.00	110315.45	0.00	0.00	0.00	0.00	0.00	443.47	0.00	1.39	1.87	0.00	283.86	
Oct-20	109515.43	549.29	0.00	0.00	108966.14	0.00	0.00	0.00	0.00	0.00	223.00	0.00	0.56	1.46	0.00	324.27	
Total	587109.24	11902.78	77536.53	0.00	497120.64	0.00	0.00	0.00	0.00	0.00	2393.71	0.00	6.95	17.54	3.60	10030.28	

Total C&D waste generated	587109.24	tonne	a1=b+c+d+e+f+g+h+i+j+k+l+m
Total C&D waste generated (excluding excavated materials)	11902.78	tonne	a2=c+d+e+f+g+h+i+j+k+l+m
Total recycled C&D waste	2418.19	tonne	a3=c+d+e+h+i+j+k
% of recycled C&D waste for BEAM Plus MA10 or MA11	20.32	%	a4=a3/a2 x 100%

- Notes:
- (1) Metal, paper & plastic were collected by recycler.
  - (2) The performance target of waste recycling are specified in the Contract.
  - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
  - (5) Broken concrete for recycling into aggregates.
  - (6) Excavated materials/waste will **NOT** be considered as part of construction waste. It should be excluded in the calculation.
  - (7) Disposal of inert waste to public fill or sorting facilities will **NOT** be considered as recycled waste.
  - (8) Disposal record for September 2020 and October 2020 have been updated according to the latest information from contractor.

Contract No. BD3/4091/19

Proposed Composite Development at N.K.I.L. 6607 Shing Kai Road, Kai Tak, Kowloon



Monthly Summary Waste Flow Table for 2020

Month	Actual Quantities of Inert C&D Materials Generated Monthly										Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated		Broken Concrete (see Note 2)		Reused in the Contract		Reused in other Projects		Disposed as Public Fill		Metals		Paper / cardboard packaging		Plastics (see Note 1)		Chemical Waste		Other, e.g. general refuse	
	(in '000 m <sup>3</sup> )		(in '000 m <sup>3</sup> )		(in '000 m <sup>3</sup> )		(in '000 m <sup>3</sup> )		(in '000 m <sup>3</sup> )		(in '000 kg)		(in '000 kg)		(in '000 kg)		(in '000 m <sup>3</sup> )		(in '000 m <sup>3</sup> )	
	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.
Jan																				
Feb																				
Mar																				
Apr																				
May																				
Jun																				
Sub-total	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Jul	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Aug	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Sep	0.26	0.10	0.00	0.00	0.00	0.00	0.00	0.00	0.20	0.10	0.05	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Oct	0.86	0.94	0.00	0.00	0.00	0.00	0.00	0.00	0.80	0.94	0.05	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Nov																				
Dec																				
Total	1.11	1.05	0.00	0.00	0.00	0.00	0.00	0.00	1.00	1.05	0.10	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Notes : (1) Plastics refer to plastic bottles / container, plastic sheets / foam from packaging material.

(2) Broken concrete for recycling into aggregates.

## Appendix J. Environmental Licences and Permits

**Table J.1: Summary of Environmental Licences and Permits Status (KTSP)**

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	441733	25 Jan 2019	29 Jan 2019	N/A	N/A
3	Construction Waste Disposal Account (Main)	7033182	12 Feb 2019	12 Feb 2019	N/A	N/A
4	Construction Waste Disposal Account (Vessel)	7033555	8 Jul 2020	13 Jul 2020	11 Nov 2020	Issued
5	Registration as a Chemical Waste Producer	WPN5213-286-H3906-02	29 Jan 2019	12 Feb 2019	N/A	N/A
6	Discharge Licence under WPCO	WT00034082-2019	15 Feb 2019	26 Jun 2019	30 Jun 2024	Issued
7	Construction Noise Permit (Percussive Piling)	PP-RE0027-20	10 Jul 2020	31 Jul 2020	19 Jan 2021	Superseded by PP-RE0044-20 on 3 Nov 2020
8	Construction Noise Permit (Percussive Piling)	PP-RE0044-20	15 Oct 2020	3 Nov 2020	27 Apr 2021	Issued
9	Construction Noise Permit (Construction Works, Barging Point)	GW-RE0462-20	15 May 2020	5 Jun 2020	21 Nov 2020	Superseded by GW-RE0910-20 on 3 Nov 2020
10	Construction Noise Permit (Construction Works, Southern Site)	GW-RE0714-20	10 Aug 2020	1 Sep 2020	28 Feb 2021	Superseded by GW-RE0916-20 on 3 Nov 2020
11	Construction Noise Permit (Construction Works, Northern Site)	GW-RE0720-20	10 Aug 2020	4 Sep 2020	23 Feb 2021	Superseded by GW-RE0911-20 on 3 Nov 2020
12	Construction Noise Permit (Construction Works, Barging Point)	GW-RE0910-20	14 Oct 2020	22 Nov 2020	20 May 2021	Issued

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
13	Construction Noise Permit (Construction Works, Northern Site)	GW-RE0911-20	14 Oct 2020	3 Nov 2020	27 Apr 2021	Issued
14	Construction Noise Permit (Construction Works, Southern Site)	GW-RE0916-20	14 Oct 2020	3 Nov 2020	27 Apr 2021	Issued

**Table J.2: Summary of Environmental Licences and Permits Status (H/O Development)**

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	458255	17 Jul 2020	17 Jul 2020	N/A	N/A
3	Construction Waste Disposal Account (Main)	7037993	5 Aug 2020	5 Aug 2020	N/A	N/A
4	Registration as a Chemical Waste Producer	WPN5113-286-C1286-03	17 Jul 2020	10 Sep 2020	N/A	N/A
5	Discharge Licence under WPCO	N/A	17 Jul 2020	N/A	N/A	Pending

# Appendix K. Environmental Mitigation Measures Implementation Status

## Air Quality – Recommended Mitigation Measures

Air Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Good housekeeping to minimize dust generation, e.g. by properly handling and storing dusty materials	✓	✓
• Store cement in shelter with 3 sides and the top covered by impervious materials if the stack exceeds 20 bags	✓	✓
• Cement delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed	N/A	N/A
• Loading, unloading, transfer, handling or storage of bulk cement should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system	✓	P
• Dusty materials (e.g. debris) should be wetted by misting / water-spraying before any loading, unloading, transfer or transport operation	✓	✓
• Any skip hoist for material transport should be fully enclosed by impervious sheeting	✓	N/A
• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously	P	✓
• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities to maintain the entire surface wet	✓	✓
• Excavation area should be minimized as far as possible	✓	✓
• Stockpile of dusty materials should not be extended beyond the pedestrian barriers, fencing or traffic cones	✓	✓
• Excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet, and then removed, backfilled or reinstated where practicable within 24 hours of the excavation or unloading	P	✓
• Dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads	✓	✓
• Properly fitted side and tail boards are necessary for any vehicle with open load area	✓	✓
• While transporting materials that potentially create dust (e.g. debris), materials should not be loaded higher than side and tail boards, and should be fully covered by tarpaulin or similar materials which extend at least 300 mm over the edges of the side and tail boards to prevent leakage.	✓	N/A
• Limit the maximum vehicle speed within the site to 10km/hr	✓	✓
• Haulage and delivery vehicles should be confined to designated roads	✓	✓
• Every main haul road should either be 1.) paved with concrete and kept clear of dusty materials, or 2.) sprayed or watered to maintain the entire road surface wet	P	✓
• All on-site unpaved roads should be compacted and kept free of loose materials as possible	✓	✓
• Provide vehicle washing (e.g. wheel washing bay & high pressure water jet where practicable) at every vehicle exit point for cleaning vehicle body and wheels	✓	✓
• The vehicle washing area and the road between washing area and site exit should be paved with concrete, bituminous or other hardcores	✓	✓
• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials.	✓	✓
• Dusty materials on every vehicle's body and wheels should be removed in washing area before leaving the site	✓	✓



• Regular maintenance of all plant equipment	✓	✓
• Throttle down or switch off unused machines or machine in intermittent use	✓	✓
• If the site is adjacent to area where accessible to the public (e.g. road and service lane etc.), hoarding of not less than 2.4 m high from ground level should be erected along the adjoining the entire length of that portion of the site boundary, except for a site entrance or exit. The hoarding should be well maintained throughout the construction period.	✓	✓
• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding	N/A	N/A
• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies	✓	✓
• Carry out air quality monitoring throughout the construction period	✓	✓
• Carry out weekly site inspection to audit the implementation of mitigation measures	✓	✓
• Regular watering once per hour on exposed worksites and haul road with an equivalent intensity of not less than 1.3L/m <sup>3</sup> to achieve 91.7% dust removal efficiency.	P	✓
• Provision of electrical vehicle (EV) charging facilities in at least one-third of the car parking spaces for private cars. Provision of EV charging enabling facilities in all car parking spaces provided for private cars.	✓	N/A
<b>Non-Road Mobile Machinery (NRMMS)</b>		
• All NRMMS operated on-site are approved or exempted (as the case may be) and affixed with the requisite approval/exemption labels under the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation or are in the process of application for such approval/exemption during the relevant grace period.	P	✓

## Noise – Recommended Mitigation Measures

Noise Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Adopt good site practice, such as throttle down or switch off equipment unused or intermittently used between works	✓	✓
• Regular maintenance of equipment to prevent noise emission due to impair	✓	✓
• Position mobile noisy equipment in locations away from NSRs and point the noise sources to directions away from NSRs	✓	✓
• Use silencer or muffler for equipment	P	✓
• Make good use structures for noise screening	✓	✓
• Use Quality Powered Mechanical Equipment (QPME) and quiet equipment which produces lower noise level.	✓	✓
• Erect movable noise barrier of 3m height to shed large plant equipment (e.g. breaker, backhoe & mobile crane) or hand-held items (e.g. poker, wood saw, power rammer & compactor) near low-rise NSR. Where necessary, special design (e.g. with noise absorbing material or bend top) should be adopted. The barrier's length should be at least five times greater than its height, and the minimum surface density is 10 kg/m <sup>2</sup> . Alternatively, acoustic shed, enclosure or silencer (for generator, air compressor and concrete pump) or acoustic mat (for piling) can be adopted.	✓	N/A
• Carry out regular site inspection to audit the implementation of mitigation measures	✓	✓
• Carry out noise monitoring throughout the construction period	✓	✓

## Water Quality – Recommended Mitigation Measures

Water Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted.	P	✓
• Install perimeter channels in the works areas to intercept runoff from boundary prior to the commencement of any earthwork	✓	✓
• To prevent storm runoff from washing across exposed soil surfaces, intercepting channels should be provided.	✓	✓
• Drainage channels are required to convey site runoff to sand/silt traps and oil interceptors. Provision of regular cleaning and maintenance to ensure the normal operation of these facilities throughout the construction period.	✓	✓
• Any practical options for the diversion and realignment of drainage should comply with both engineering and environmental requirements	✓	✓
• Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the existing WSD saltwater intake and EMSD cooling water intake.	✓	✓
• The following good site measures should be adopted for the use of the existing barging facilities being operated by the MTR SCL Project: - All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. - All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material. - Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site. - Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. - Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation. Whole construction site Contractor P WPCO, EIAO-TM Page	N/A	N/A
• The runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS.	✓	N/A
• Reuse and recycling of the treated effluent from construction site runoff.	✓	✓
• Weekly site audit should be carried out to check the implementation status of the recommended water quality impact mitigation measures throughout construction period.	✓	✓
• The construction programme should be properly planned to minimise soil excavation, if any, in rainy seasons.	✓	✓
• Any exposed soil surfaces should be properly protected to minimise dust emission.	✓	✓
• In areas where a large amount of exposed soils exist, earth bunds or sand bags should be provided.	✓	✓
• Exposed stockpiles should be covered with tarpaulin or impervious sheets at all times.	✓	✓
• The stockpiles of materials should be placed at locations away from any stream courses so as to avoid releasing materials into the water bodies.	✓	✓
• Final surfaces of earthworks should be compacted and protected by permanent work.	✓	✓
• Haul roads should be paved with concrete and the temporary access roads protected using crushed stone or gravel, wherever practicable.	✓	✓
• Wheel washing facilities should be provided at all site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.	✓	P
• Good site practices should be adopted to keep the site dry and tidy, such as clean the rubbish and litter on the construction sites.	✓	✓
• Adequate temporary site drainage and pumping should be provided, if necessary.	P	✓
• Provide sufficient temporary toilets in the works areas. The toilet facilities should be more than 30 m from any watercourse. A licensed waste collector should be deployed to clean the temporary toilets on a regular basis.	✓	✓
• Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project.	✓	N/A

<ul style="list-style-type: none"> <li>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>Clean the construction sites on a regular basis.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Oil interceptor in car parking area shall be designed and constructed according to Practice Note for Authorized Persons, Registered Structural Engineers and Registered Geotechnical Engineers, APP-46 (PNAP 124)</li> </ul>	N/A	N/A
<ul style="list-style-type: none"> <li>Provide two sequential storage tanks to contain surface water with residual fertilizers and pesticides and third holding tank for incidental rainstorm</li> </ul>	N/A	N/A
<b>Sewerage and Sewage Treatment Implications</b>		
<ul style="list-style-type: none"> <li>Implementation of Sewer No. 1 and Sewer No.2 as proposed in Sections 7.2.2 - 7.2.3 of the EIA Report</li> </ul>	✓	✓

## Waste Management – Recommended Mitigation Measures

Waste Management Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Inert C&amp;D materials (or public fills) will be used to form the ramps and other filling area as far as civil engineering design permits.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The contractor should formulate waste management measures on waste minimization, storage, handling and disposal in a Waste Management Plan as part of Environmental Management Plan.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Adopt good site practice as follows:                             <ul style="list-style-type: none"> <li>Provide training to workers on site cleanliness, waste management (waste reduction, reuse and recycle) and chemical handling procedures</li> <li>Provide sufficient waste collection points and regular removal</li> <li>Cover waste materials with tarpaulin or in enclosure during transportation</li> <li>Maintain drainage systems, sumps and oil interceptors</li> <li>Sort out chemical waste for proper handling and treatment onsite or offsite</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Adopt waste reduction measures as follows:                             <ul style="list-style-type: none"> <li>Allocate area/containers for sorting, recovering and storing waste for reuse, recycle or disposal (e.g. demolition debris and excavated materials, general refuse like aluminium cans.) Remove waste from the Site for sorting once generated if no suitable space can be identified.</li> <li>Allocate area for proper storage of construction materials to prevent contamination</li> <li>Minimize wastage through careful planning and avoiding over-purchase of construction materials</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Store waste materials properly as follows:                             <ul style="list-style-type: none"> <li>Avoid contamination by proper handling and storing waste</li> <li>Prevent erosion by covering waste</li> <li>Apply water spray on excavated materials</li> <li>Maintain and clean storage area regularly</li> <li>Sort and stockpile different materials at designated location to enhance reuse</li> </ul> </li> </ul>	P	✓
<ul style="list-style-type: none"> <li>Apply for relevant waste disposal permits in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28), Dumping at Sea Ordinance (Cap. 466).</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire licensed waste disposal contractors for waste collection and removal. Dispose waste at licensed waste disposal facilities.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Implement trip-ticket system for recording the amount of waste generated, recycled and disposed, including chemical wastes</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Reduce water content in wet spoil generated from piling work by mixing with dry materials. Only dispose treated spoil with less than 25% dry density to Public Fill Reception Facilities</li> </ul>	✓	✓

<ul style="list-style-type: none"> <li>Dispose dry waste or waste with less than 70% water content by weight to landfill</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Follow the Code of Practice on the Packaging, Labelling and Storage of Chemical Waste as follows:                             <ul style="list-style-type: none"> <li>Store chemical wastes with suitable containers. Seal and maintain the container to avoid leakage or spillage during storage, handling and transport</li> <li>Label chemical waste containers in both English and Chinese with instructions in accordance to Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation</li> <li>The container capacity should be smaller than 450 litres unless agreed by the EPD</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Comply with the requirement of the chemical storage area:                             <ul style="list-style-type: none"> <li>Store only chemical waste and label clearly the chemical characters of the waste</li> <li>Have at least 3 sides enclosed and protected from rainfall with cover</li> <li>Provide sufficient ventilation</li> <li>Have impermeable floor and has bunds to contain 110% of the capacity of the largest container or 20% of the total volume of the stored waste in the area, whichever is larger</li> <li>Adequately spaced incompatible materials</li> </ul> </li> </ul>	P	P
<ul style="list-style-type: none"> <li>Transfer used lubricants, waste oils and other chemicals to oil recycling companies, if possible, and empty oil drums for reuse or refill. No direct or indirect discharge is permitted</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire licensed chemical waste disposal contractors for waste collection and removal. Dispose chemical waste at the approved Chemical Waste Treatment Centre at Tsing Yi or other licensed facility</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire reputable waste collector to separately collect and dispose general refuse from other wastes. Cover the waste to prevent being blown away</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The hauling of C&amp;D materials shall follow established environmental mitigation measures as stated in Practice Note for Registered Contractors No. 17 "Control of Environmental Nuisance from Construction Sites" issued by the Buildings Department</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Provide recycling bins for sorting out recyclables for collection by recycling companies. Non-recyclables should be removed to designated landfills every day by licensed collectors to prevent environmental and health nuisance.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Organize training and reminders to site staff on waste minimization through avoidance and reduction, reusing and recycling</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Bentonite slurry which will not be reused shall be disposed of from the Site as soon as possible. Residual used dewatered bentonite slurry should be disposed to a public filling area and liquid bentonite slurry if mixed with inert fill material should be disposed to a public filling area.</li> </ul>	N/A	N/A
<ul style="list-style-type: none"> <li>If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the waste such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport the chemical wastes.</li> <li>The licensed collector shall deliver the waste to the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Carry out weekly site inspection to check the implementation status of the recommended waste management measures.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The barging of C&amp;DM for this Project shall use the existing Kai Tak Barging Facility (KTBF), or otherwise approved by the Director.</li> </ul>	N/A	N/A

## Ecology – Recommended Mitigation Measures

Ecology Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Erection of hoarding, fencing or provision of clear demarcation of work zone</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Designate areas for placement of equipment, building materials and wastes away from drainage channels</li> </ul>	✓	✓

<ul style="list-style-type: none"> <li>Carry out weekly site inspection to check the implementation status and the effectiveness of the proposed mitigation measures</li> </ul>	✓	✓
---	---	---

## Landscape and Visual – Recommended Mitigation Measures

Landscape and Visual Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Construction Lighting Control                             <ul style="list-style-type: none"> <li>All security floodlights for construction sites should be equipped with adjustable shields, frosted diffusers and reflective covers, and be controlled to minimize light pollution and night-time glare to the visual sensitive receivers (VSRs).</li> </ul> </li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>Temporary Landscape Treatments                             <ul style="list-style-type: none"> <li>Including vertical greening, pot planting and application of green roofing to site offices, Hydroseeding of site formation areas and short term greening of site boundaries and land not immediately developed.</li> </ul> </li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>Decoration of Hoarding                             <ul style="list-style-type: none"> <li>Erection of screen hoardings should be designed appropriately to be compatible with the existing urban context, either brightly and imaginatively or with visually unobtrusive design and colours where more appropriate.</li> </ul> </li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>All security floodlights for construction sites shall be equipped with adjustable shield, frosted diffusers and reflective covers, and be carefully controlled to minimize light pollution and night-time glare to nearby receivers</li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>Site inspection should be undertaken once every two weeks.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Compensatory Tree Planting                             <ul style="list-style-type: none"> <li>A new parkland area is created in the project development to be used for the implementation of compensatory tree planting to offset the net loss of key landscape resources. It is recommended that 340 trees be planted in this regard and a compensatory tree planting proposal outlining the locations of tree compensation will be submitted separately in seeking relevant government department's approval in accordance with DEVB TC No.7/2015.</li> </ul> </li> </ul>	N/A	N/A

## Other – Recommended Mitigation Measures

<ul style="list-style-type: none"> <li>Relevant environmental permits/licences should be posted at all vehicle entrances/exits.</li> </ul>	✓	✓
--	---	---

Legend:

- ✓ Implemented
- x Not implemented
- P Partially implemented
- N/A Not applicable

## Appendix L. Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

**Table L.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions**

Reporting Period	Complaints	Notifications of Summons	Successful Prosecutions
This reporting period (October 2020)	1	0	0
From commencement data of construction to end of reporting month	7	0	0

# Appendix M. Complaint Investigation Report

**Interim Report on Complaint Investigation**

RECEIPT OF COMPLAINT		Ref: COM_0007	
Date:	6 October 2020		
Time:	15:20		
From:	PS Chan (Hip Hing Construction Limited)		
Via:	Email		
Contact no.:	-		
COMPLAINANT			
Name:	Ms. Viviana T.S. Tong	Address:	-
Contact no.:	2117 7572		
DETAILS OF COMPLAINT			
Date:	11 September 2020		
Time:	-		
Parameter:*	<del>Dust</del>	Noise	Water Other (specify):
Description:	<p>- Complaint of soil/muddy water at To Kwa Wan Typhoon Shelter on 10 September 2020.</p> <p>- Please closely monitor the effluent of your wastewater treatment plants, provide sufficient wastewater treatment capacity and implement practicable measures to prevent discharge of muddy water including surface run-off from your site. Please ensure the works comply with all relevant environmental legislations.</p>		
INVESTIGATION RESULT & RESPONSE			
ET, IEC and SOR notified on:	6 October 2020		
Investigation conducted on:	8 October 2020		
Result of investigation:	<p>1. According to contractor's photo record on 10 September 2020, no polluting muddy water discharge was observed at nearby seashore near To Kwa Wan Typhoon Shelter. (Photos 1a &amp; 1b)</p> <p>2. Site investigation was carried out on 8 October 2020, and details of findings summarised as follow:</p> <p>- No pollution effluent discharge was observed at nearby seashore near To Kwan Wan Typhoon Shelter. (Photo 2)</p> <p>- No pollution effluent discharge was observed at nearby seashore near barging point. (Photo 3)</p>		
RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS			
Environmental remediation action implemented and maintained summaries as follow:			
<p>1. Regular monitoring of water quality at effluent discharge on site. (Photo 4)</p> <p>2. Silt curtain has been provided and kept good maintenance near barging point. (Photo 5)</p> <p>3. Sedimentation tank has been provided for treatment and temporary storage of the wastewater. (Photo 6)</p> <p>4. Regular sludge removal of the sedimentation tank has been conducted. (Photo 7)</p>			
Prepared by:	Sunny Chan	Title:	Environmental Team Leader
Signature:		Date:	8 October 2020



**ATTACHMENTS**

**Photo Records:**



Photo 1a: Box Culvert near To Kwa Wan Typhoon Shelter (10 September 2020)



Photo 1b: Nearby Seashore near To Kwa Wan Typhoon Shelter (10 September 2020)



Photo 2: Seashore near To Kwa Wan Typhoon Shelter (8 October 2020)



Photo 3: Seashore near Barging Point (8 October 2020)



Photo 4: Regular Monitoring of Discharge at Effluent Tank



Photo 5: Deposition of Silt curtain near Barging Point.



Photo 6: Provision of Sedimentation Tank for Temporary Storage of Wastewater on Site



Photo 7: Regular Sludge Removal for the Sedimentation Tank on Site.
