



**Agreement No. CE 30/2018 (EP)
Environmental Team for Kai Tak Sports Park –
Design and Construction**

Quarterly EM&A Report (Apr 2023 – Jun 2023)

July 2023

Culture, Sports and Tourism
Bureau
Kai Tak Sports Park Project Office
1/F, Block A
Kai Tak Sports Park Site Office
Muk Tai Street
Kai Tak, Kowloon

Agreement No. CE 30/2018 (EP)
Environmental Team for Kai Tak Sports Park –
Design and Construction

Quarterly EM&A Report (Apr 2023 – Jun 2023)

July 2023



Environmental Permit No. EP-544/2017

Kai Tak Sports Park - Investigation

Independent Environmental Checker Verification


Reference Document/Plan

Document/ Plan to be Certified / Verified:	Quarterly EM&A Report No. 17 (April to June 2023)
Date of Report:	28 July 2023
Date received by IEC:	28 July 2023

Reference EP Condition / EM&A Manual

EM&A Manual (AEIAR-204/2017)	Sections 2.5.1 (v) & 14.1.1
The ET should prepare monthly, quarterly and final EM&A reports to summarize environmental performance and to anticipate future key issues.	
The ET shall prepare baseline monitoring report, monthly EM&A reports, quarterly EM&A report and final EM&A report. They shall be submitted to the EPD in paper and electronic formats in a timely manner.	

IEC Verification

I hereby verify that the above referenced document/ plan complies with the above referenced condition of EP-544/2017/EM&A Manual.	
	
Ms Mandy To Independent Environmental Checker	Date: 28 July 2023

Our ref: 0500384_IEC Verification Cert_KTSP_Quarterly EM&A Rpt No.17.docx



Culture, Sports and Tourism Bureau
The Government of the Hong Kong Special Administrative Region
of the People's Republic of China



Environmental Permit No. EP- 544/2017

Kai Tak Sports Park – Investigation

Environmental Team Leader Certification

Reference Document /Plan

Document/ Plan to be Certified:	Quarterly EM&A Report (Apr 2023 – Jun 2023)
Date of Report:	28 July 2023
Date received by ETL:	28 July 2023

Reference EP Condition

EM&A Manual (AEIAR-204/2017)	Sections 2.5.1 (v) & 14.1.1
------------------------------	-----------------------------

The ET should prepare monthly, quarterly and final EM&A reports to summarize environmental performance and to anticipate future key issues.

The ET shall prepare baseline monitoring report, monthly EM&A reports, quarterly EM&A report and final EM&A report. They shall be submitted to the EPD in paper and electronic formats in a timely manner.

ETL Certification

I hereby certify that the above reference document complies with the above referenced condition of EP-544/2017.

Mr Sunny Chan
Environmental Team Leader

Date: 28 July 2023

Contents

Executive Summary	1
1 Project Information	6
1.1 Project Organisation	6
1.2 Works Area and Construction Programme	6
1.3 Construction Works undertaken during the Reporting Period	7
2 Summary of EM&A Requirement	8
2.1 EM&A Requirement	8
2.2 Air Quality Monitoring Parameters, Frequency and Duration	8
2.3 Air Quality Monitoring Locations	8
2.4 Action and Limit Levels for Air Quality Monitoring	9
2.5 Wind Data	9
2.6 Noise Monitoring Parameters, Frequency and Duration	10
2.7 Noise Monitoring Locations	10
2.8 Action and Limit Levels for Noise Monitoring	11
3 Summary of Environmental Status	12
3.1 Construction Works undertaken during the Reporting Period	12
3.2 Implementation Status of Environmental Mitigation Measures	12
3.3 Monitoring Results	12
3.4 Solid and Liquid Waste Management Status	13
3.5 Summary of Non-compliance Status	14
4 Comments, Recommendations and Conclusion	17
4.1 Comments	17
4.2 Recommendations	17
4.3 Conclusions	19

Figures

Figure 2.1: Location of Air Quality Monitoring Stations

Figure 2.2: Location of Noise Monitoring Stations

Appendices

Appendix A. Project Organization for Environmental Works

Appendix B. Location of Works Areas

Appendix C. Construction Programme

Appendix D. Event and Action Plan

Appendix E. Monitoring Data and Graphical Plots (Air Quality and Noise)

Appendix F. Wind Data

Appendix G. Waste Flow Table

Appendix H. Environmental Licences and Permits

Appendix I. Environmental Mitigation Measures Implementation Status

Appendix J. Statistics on Environmental Complaints, Notification of Summons and
Successful Prosecutions

Appendix K. Calibration Certificate

Appendix L. Complaint Investigation Report

Tables

Table 1.1: Contact Information of Key Personnel	6
Table 1.2: Construction Works undertaken during the Reporting Period	7
Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration	8
Table 2.2: Detail of Proposed Dust Monitoring Station	8
Table 2.3: Construction Dust Monitoring Locations	8
Table 2.4: Temporary Construction Dust Monitoring Location	9
Table 2.5: Action and Limit Levels for 1-hour TSP	9
Table 2.6: Noise Monitoring Parameters, Frequency and Duration	10
Table 2.7: Detail of Proposed Noise Monitoring Location	10
Table 2.8: Construction Noise Monitoring Locations	10
Table 2.9: Temporary Construction Noise Monitoring Location	11
Table 2.10: Action and Limit Level for Construction Noise	11
Table 3.1: Construction Works undertaken during the Reporting Period	12
Table 3.2: Summary of Site Inspection and Landscape Audit during the Reporting Period	12
Table 3.3: Summary of 1-hour TSP Monitoring Results during the Reporting Period	13
Table 3.4: Summary of Construction Noise Monitoring Results during the Reporting Period	13
Table 3.5: Comparison of Estimated Amount and Actual Amount of Waste Generated during the Reporting Period	13
Table 3.6: Summary of Complaints during the Reporting Period	14
Table D.1: Event and Action Plan for Construction Air Quality (Action Level)	
Table D.2: Event and Action Plan for Construction Air Quality (Limit Level)	
Table D.3: Event and Action Plan for Construction Noise	
Table H.1: Summary of Environmental Licences and Permits Status (KTSP)	
Table H.2: Summary of Environmental Licences and Permits Status (H/O Development)	
Table J.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions	

Executive Summary

This is the 17th Quarterly Environmental Monitoring & Audit (EM&A) Report for the construction phase of the Kai Tak Sports Park (KTSP) Project which summaries findings of the EM&A programme during the reporting period from 1 April 2023 to 30 June 2023 (the “reporting period”) under the Environmental Permit (No. EP-544/2017) requirement.

Environmental Monitoring and Audit Progress

The monthly EM&A programme was implemented by Environmental Team (ET) in accordance with the approved EM&A Manual. A summary of the EM&A activities during the reporting period is presented below:

Activities	Locations	Dates
Air quality impact monitoring (1-hour TSP)	AMS1-T*, AMS2, AMS4	6*, 11*, 17*, 21*, 27* Apr 2023 3*, 9*, 15*, 19*, 24*, 30* May 2023 5*, 9*, 15*, 21*, 27* Jun 2023
Noise impact monitoring (L _{eq} (30 min))	NMS1-T*, NMS2, NMS4	6*, 11*, 17*, 27* Apr 2023 3*, 9*, 15*, 24*, 30* May 2023 5*, 15*, 21*, 27* Jun 2023
Weekly environmental site inspections	Kai Tak Sports Park Project Site	4, 12, 19, 25 Apr 2023 3, 10, 17, 23, 31 May 2023 7, 14, 20, 28 Jun 2023
Bi-weekly landscape and visual site inspections	Kai Tak Sports Park Project Site	4, 19 Apr 2023 10, 23 May 2023 7, 20 Jun 2023

***Note:**

During the reporting period, monitoring station, Hong Kong Society for the Blind Workshop (AMS1 and NMS1), was no longer open for impact monitoring from 1 September 2022, due to relocation of the Hong Kong Society for the Blind Workshop.

Agriculture, Fisheries and Conservation Department Kowloon Animal Management Centre (AMS1-T and NMS1-T) were proposed to conduct dust monitoring and noise impact monitoring during the reporting period.

Details of temporary alternative monitoring locations are presented in Temporary Alternative Proposal for Monitoring Station as proposed by ET and agreed by IEC dated 6 January 2021.

Breaches of Action and Limit Levels

Air Quality

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1-T, AMS2 and AMS4 during the reporting period.

Noise

Two noise related complaints were received during the reporting period. Two Action Level exceedances for noise were triggered during the reporting period.

No Limit Level exceedances of noise at NMS1-T, NMS2 and NMS4 was recorded during the reporting period.

Complaint Log

There were three complaints received in relation to the environmental impact during the reporting period.

Summary of Complaints in the Reporting Month

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
25 Apr 2023	16 Apr 2023	<p>- Complaint of construction noise from the construction site of Kai Tak Sports Park in the night time (around 20:xx) on 13/4/2023 and 15/4/2023.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	<ol style="list-style-type: none"> 1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents. 2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. 3. Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement. 4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule. 	28 Apr 2023

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
23 May 2023	19 May 2023	- Complaint of discharging polluting wastewater from North Gate No. 4 at Muk Tai Street. - Please ensure the wastewater generated from your site to be properly treated and the discharge fulfill the conditions stipulated in the valid WPCO licence. - Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit. - Please take necessary measures to minimize the environmental nuisance arising from the construction site.	1. Self-monitoring of wastewater discharge sample had been conducted and reported monthly. 2. Regular pest control measures had been provided near North Gate No. 4 Area.	24 May 2023

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
5 Jun 2023	31 May 2023	- Complaint of construction noise (piling work) from construction sites near Sung Wong Toi Road starting around 08:00am on weekdays - Please take necessary environmental measures to minimize the environmental nuisance arising from the construction site.	1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents. 2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. 3. Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement. 4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule.	7 Jun 2023

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during this reporting period.

Reporting Changes

There was no reporting change during the reporting period.

1 Project Information

1.1 Project Organisation

The organisation chart and lines of communication with respect to the on-site environmental management structure of the key personnel are shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1: Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Project Proponent (Home Affairs Bureau)	Project Director (Sports Park)	Edwin Wong	3586 3403	3586 0591
Supervising Officer's Representative (Home Affairs Bureau)	Senior Engineer	Keith Man	3586 3149	3586 0591
Environmental Team (Mott MacDonald Hong Kong Limited)	Environmental Team Leader	Sunny Chan	2828 5962	2827 1823
	Deputy Environmental Team Leader	Ken Wong	2828 5757	2827 1823
Independent Environmental Checker (ERM Hong Kong Limited)	Independent Environmental Checker	Mandy To	2271 3000	3015 8052
Contracted Party (Kai Tak Sports Park Limited)	Assistant Contract Manager	Eric Chung	3552 5003	2845 9295
	Environmental Officer	Gary Yim	3552 5013	3552 5099
Hotel and Office Development				
Project Manager (Sanon Limited)	Senior Group Project Director	David Lee	2910 8368	2815 9949
	Project Manager	William Chan	2910 8363	2815 9949
Project Architect (P&T Architects & Engineers Limited)	Project Architect	Patrick Chan	2832 7205	-
Contractor (Hip Hing Construction Co. Ltd.)	Project Manager	Ian Ku	6099 9686	-
24-hour Community Liaison Hotline	-	-	5587 6112	-

1.2 Works Area and Construction Programme

The construction works commenced on 8 April 2019. The works area of the Project is shown in **Appendix B**. The Construction Works Programme of the Project is provided in **Appendix C**.

1.3 Construction Works undertaken during the Reporting Period

A summary of construction activities undertaken during this reporting period is presented below:

Table 1.2: Construction Works undertaken during the Reporting Period

April 2023	May 2023	June 2023
KTSP		
<ul style="list-style-type: none"> • Rebar fixing; • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction 	<ul style="list-style-type: none"> • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction 	<ul style="list-style-type: none"> • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction
H/O Development		
<ul style="list-style-type: none"> • Excavation; • Rebar fixing; and • Concreting. 	<ul style="list-style-type: none"> • Excavation; and • Concreting. 	<ul style="list-style-type: none"> • Excavation; and • Concreting.

2 Summary of EM&A Requirement

2.1 EM&A Requirement

In accordance with the EM&A Manual of the Project, the EM&A programme was established to assure compliance with the standards and predictions in the EIA study involving the construction and operation of the Project. The environmental performance was routinely monitored and audited for evaluating the effectiveness of the recommended mitigation measures or remedial action. Impact air quality and noise monitoring were required for the Project.

Air Quality

2.2 Air Quality Monitoring Parameters, Frequency and Duration

Table 2.1 summarises the monitoring parameters, frequency and duration of impact air quality monitoring.

Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
1-hour TSP	3 times every six-days

2.3 Air Quality Monitoring Locations

According to the EM&A Manual, a total of five air quality monitoring stations were identified for impact monitoring. Of these, two air quality sensitive receivers AMS3 and AMS5 are planned residential use and were currently not available for impact monitoring during the reporting period.

Monitoring station AMS4, the originally planned residential use at Kai Tak Area 1K Site 3 (i.e. The Henley) has been in occupation in July 2022. The detail of the proposed monitoring station is shown as follow:

Table 2.2: Detail of Proposed Dust Monitoring Station

Monitoring Station	Description in EM&A Manual	Proposed Monitoring Station
AMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Rooftop of Retail Building in front of The Henley

Table 2.3 describes the impact air quality monitoring stations and **Figure 2.1** shows their locations.

Table 2.3: Construction Dust Monitoring Locations

Monitoring Station	Location	Status
AMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Air Sensitive Receiver
AMS2	Sky Tower, Podium of Tower 7	Existing Air Sensitive Receiver
AMS4	Retail Building in front of The Henley, Rooftop	Existing Air Sensitive Receiver
AMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Air Sensitive Receiver
AMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Air Sensitive Receiver

During the reporting period, monitoring station AMS1 was no longer open for impact monitoring from 1 September 2022, due to relocation of the Hong Kong Society for the Blind Workshop.

Temporary air quality monitoring station, AMS1-T, was used to conduct dust monitoring in September 2022. Details of temporary alternative monitoring locations are presented in Temporary Alternative Proposal for Monitoring Station as proposed by ET and agreed by IEC dated 6 January 2021.

The details of temporary monitoring station are described in **Table 2.4** and the location of temporary monitoring station is shown in **Figure 2.1**.

Table 2.4: Temporary Construction Dust Monitoring Location

Monitoring Station	Location	Status
AMS1-T	Agriculture, Fisheries and Conservation Department Kowloon Animal Management Centre, 102 Sung Wong Toi Road	Existing Air Sensitive Receiver

2.4 Action and Limit Levels for Air Quality Monitoring

The Action and Limit Levels for 1-hr TSP are provided in **Table 2.5**.

Table 2.5: Action and Limit Levels for 1-hour TSP

Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1 – Hong Kong Society for the Blind Workshop, Roof Floor	283	500
AMS2 – Sky Tower, Podium of Tower 7	280	500
AMS3 - Kai Tak Area 2B Site 4 (2B4) (residential use)	287*	500
AMS4 - Kai Tak Area 1K Site 3 (1K3) (residential use)	287*	500
AMS5 - Kai Tak Area 1L Site 3 (1L3) (residential use)	287*	500

*Remarks: the Action Level for AMS3, AMS4 and AMS5 were derived from an alternative monitoring station AMS3-4-5 during the baseline monitoring.

The event and action plan is provided in **Appendix D**.

2.5 Wind Data

Wind data at Kai Tak automatic weather station collected from the Hong Kong Observatory (HKO) were used for the air quality monitoring for recording wind speed and wind direction. It is considered that the wind data obtained at the existing Kai Tak wind station are representative of the Project area and could be used for undertaking the construction phase baseline and impact air quality monitoring programme for the Project.

The detail of the wind data is shown in **Appendix F**.

Noise

2.6 Noise Monitoring Parameters, Frequency and Duration

Table 2.6 summarises the monitoring parameters, frequency and duration of impact noise monitoring.

Table 2.6: Noise Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
30-minutes measurement at each monitoring station between 0700 and 1900 on normal weekdays (Monday to Saturday). L _{eq} , L ₁₀ and L ₉₀ would be recorded.	At least once per week

2.7 Noise Monitoring Locations

According to the approved EM&A Manual, a total of seven noise monitoring stations were identified for the impact monitoring locations. Of these, four noise sensitive receivers NMS1A, NMS2A, NMS3 and NMS5 are planned residential use and were currently not available for impact monitoring during the reporting period.

Monitoring station NMS4, the originally planned residential use at Kai Tak Area 1K Site 3 (i.e. The Henley) has been in occupation in July 2022. The detail of the proposed monitoring stations are shown as follow:

Table 2.7: Detail of Proposed Noise Monitoring Location

Monitoring Station	Description in EM&A Manual	Proposed Monitoring Station
NMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Rooftop of Retail Building in front of The Henley (Façade Measurement)

Table 2.8 describes the details of the monitoring stations and **Figure 2.2** shows the locations of noise monitoring stations.

Table 2.8: Construction Noise Monitoring Locations

Monitoring Station	Location Description	Status
NMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Noise Sensitive Receiver
NMS2	Sky Tower, Podium of Tower 7	Existing Noise Sensitive Receiver
NMS4	Retail Building in front of The Henley, Rooftop	Existing Noise Sensitive Receiver
NMS1A	Sung Wong Toi Road Public Housing Site	Planned Noise Sensitive Receiver
NMS2A	Sung Wong Toi Road CDA Site (mixed use)	Planned Noise Sensitive Receiver
NMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Noise Sensitive Receiver
NMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Noise Sensitive Receiver

During the reporting period, monitoring station NMS1 was no longer open for impact monitoring from 1 September 2022, due to relocation of the Hong Kong Society for the Blind Workshop.

Temporary noise monitoring station, NMS1-T, was used to conduct noise monitoring from September 2022. Details of temporary alternative monitoring locations are presented in Temporary Alternative Proposal for Monitoring Station as proposed by ET and agreed by IEC dated 6 January 2021. The details of temporary monitoring station are described in **Table 2.9** and the location of noise monitoring station is shown in **Figure 2.2**

Table 2.9: Temporary Construction Noise Monitoring Location

Monitoring Station	Location Description	Status	Type of Measurement
NMS1-T	Agriculture, Fisheries and Conservation Department Kowloon Animal Management Centre, 102 Sung Wong Toi Road	Existing Noise Sensitive Receiver	Façade

Action and Limit Levels for Noise Monitoring

The Action and Limit Levels for construction noise are defined in **Table 2.10**

Table 2.10: Action and Limit Level for Construction Noise

Monitoring Station	Time Period	Action Level	Limit Level
NMS1 NMS2 NMS4	0700 – 1900 hours on normal weekdays	When one documented complaint is received	75 dB(A)

The event and action plan is provided in **Appendix D**.

3 Summary of Environmental Status

3.1 Construction Works undertaken during the Reporting Period

A summary of construction activities undertaken during this reporting period is presented below:

Table 3.1: Construction Works undertaken during the Reporting Period

April 2023	May 2023	June 2023
KTSP		
<ul style="list-style-type: none"> • Rebar fixing; • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction 	<ul style="list-style-type: none"> • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction 	<ul style="list-style-type: none"> • Mobilization and lifting; • Concreting; • Excavation; • Main Stadium pre-cast material delivery; and • Public Sports Ground drainage layer construction
H/O Development		
<ul style="list-style-type: none"> • Excavation; • Rebar fixing; and • Concreting. 	<ul style="list-style-type: none"> • Excavation; and • Concreting. 	<ul style="list-style-type: none"> • Excavation; and • Concreting.

3.2 Implementation Status of Environmental Mitigation Measures

Regular site inspections and audits were carried out to monitor the implementation of proper environmental pollution control mitigation measures for the Project. **Table 3.2** shows the summary of site inspection and audit conducted during the reporting period.

Table 3.2: Summary of Site Inspection and Landscape Audit during the Reporting Period

Activities	Locations	Dates
Weekly environmental site inspections	Kai Tak Sports Park Project Site	4, 12, 19, 25 Apr 2023 3, 10, 17, 23, 31 May 2023 7, 14, 20, 28 Jun 2023
Bi-weekly landscape and visual site inspections	Kai Tak Sports Park Project Site	4, 19 Apr 2023 10, 23 May 2023 7, 20 Jun 2023

A summary of the environmental mitigation measures implementation status is presented in **Appendix I**. Most of the necessary mitigation measures were implemented properly. A summary of the environmental licenses and permits is presented in **Appendix H**.

3.3 Monitoring Results

The monitoring results for 1-hour TSP at AMS1-T, AMS2, and AMS4 are summarized in **Table 3.3**. Detailed impact air quality monitoring results are presented in **Appendix E**. The calibration certificate for the dust meter used during monitoring is shown in **Appendix K**.

Table 3.3: Summary of 1-hour TSP Monitoring Results during the Reporting Period

Monitoring Station	Average, $\mu\text{g}/\text{m}^3$	Min, $\mu\text{g}/\text{m}^3$	Max, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1-T	65	36	124	283	500
AMS2	59	14	121	280	500
AMS4	58	29	104	287	500

There was no Action and Limit Level exceedance of 1-hr TSP level recorded at station AMS1-T, AMS2 and AMS4 by the ET during the reporting period.

The monitoring results for construction noise are summarized in **Table 3.4**. Detailed impact noise monitoring results and relevant graphical plots are presented in **Appendix E**. The calibration certificate for the noise meter used during monitoring is shown in **Appendix K**.

Table 3.4: Summary of Construction Noise Monitoring Results during the Reporting Period

Monitoring Station	Measured Noise Level L_{eq} (30 mins), dB(A)			
	Average	Min	Max	Limit Level
NMS1-T	71	70	72	75
NMS2	69	68	70	75
NMS4	65	64	70	75

No noise exceedances were recorded at stations NMS1-T, NMS2 and NMS4 by the ET during the reporting period.

3.4 Solid and Liquid Waste Management Status

The summary of waste flow table during the reporting period is detailed in **Appendix G**.

The comparison of estimated amount of waste generated for construction of the Project and actual amount generated during the reporting period is showed in **Table 3.5**.

Mitigation measures recommended in EIA Report were implemented by the Contractor as far as practicable and were considered effective in reducing the total quantity of waste generated during the reporting period.

Table 3.5: Comparison of Estimated Amount and Actual Amount of Waste Generated during the Reporting Period

Type of Waste	Estimated Amount for the Project in the EIA (m^3)	Actual Amount during Reporting Period (000kg)	Actual Amount during Reporting Period* (m^3)
Inert C&D materials (or public fills) to be disposed of	447,464	32,914	25,318
Non-inert C&D materials (or C&D waste) to be disposed of	68,110	4,867	6,084
Total C&D material of the Project	515,574	37,781	31,402

*Note:

Assumed Inert C&D waste density = 1,300 kg/m³

Assumed Non-inert C&D waste density = 800 kg/m³

3.5 Summary of Non-compliance Status

Exceedances

Air Quality

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1-T, AMS2 and AMS4 during the reporting period.

Noise

Two noise related complaints were received during the reporting period. Two Action Level exceedances for noise were triggered during the reporting period.

No Limit Level exceedances of noise at NMS1-T, NMS2 and NMS4 was recorded during the reporting period.

Complaints

There was three complaints received in relation to the environmental impact during the reporting period. Summary of complaints during the reporting period are presented in **Table 3.6**.

Table 3.6: Summary of Complaints during the Reporting Period

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
25 Apr 2023	16 Apr 2023	- Complaint of construction noise from the construction site of Kai Tak Sports Park in the night time (around 20:xx) on 13/4/2023 and 15/4/2023. - Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit. - Please take necessary measures to minimize the environmental nuisance arising from the construction site.	1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents. 2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. 3. Notice was provided to all subcontractors to follow the latest	28 Apr 2023

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
			<p>Construction Noise Permit Requirement.</p> <p>4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule.</p>	
23 May 2023	19 May 2023	<p>- Complaint of discharging polluting wastewater from North Gate No. 4 at Muk Tai Street.</p> <p>- Please ensure the wastewater generated from your site to be properly treated and the discharge fulfill the conditions stipulated in the valid WPCO licence.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	<p>1. Self-monitoring of wastewater discharge sample had been conducted and reported monthly.</p> <p>2. Regular pest control measures had been provided near North Gate No. 4 Area.</p>	24 May 2023
5 Jun 2023	31 May 2023	<p>- Complaint of construction noise (piling work) from construction sites</p>	<p>1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise</p>	7 Jun 2023

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
		near Sung Wong Toi Road starting around 08:00am on weekdays - Please take necessary environmental measures to minimize the environmental nuisance arising from the construction site.	nuisance to the nearby residents. 2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. 3. Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement. 4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule.	

Notification of Summons and Successful Prosecution

No notification of summons or prosecutions was received during the reporting period.

Statistics on notifications of summons and successful prosecutions are summarized in **Appendix J**.

4 Comments, Recommendations and Conclusion

4.1 Comments

Mitigation measures in the EM&A Manual were implemented during the reporting period. The weekly environmental site inspections ensured that all the environmental mitigation measures recommended were effectively implemented. Based on observation from the site inspections, landscape audits, and the air quality and noise impact monitoring results recorded, it was considered that mitigation measures were effective and efficient in controlling the potential impacts due to construction of the project during the reporting period.

4.2 Recommendations

During the reporting period, the following recommendations were provided:

April 2023

KTSP

- The contractor was reminded to dispose of the general refuse properly to avoid contamination.
- The contractor was reminded to maintain good housekeeping to handle dusty materials properly.
- The contractor was reminded to store recycle material properly in enclosed recycle bin.
- The contractor was reminded to replace the NRMM label.
- The contractor was reminded to clear the general refuse regularly.

H/O Development

- The contractor was reminded to provide water spraying on haul road to maintain wet surface.
- The contractor was reminded to provide covering for the stockpile and store the stockpile properly away from site entrance.
- The contractor was reminded to clear the general refuse regularly.
- The contractor was reminded to replace the NRMM label.

May 2023

KTSP

- The contractor was reminded to clear the general refuse regularly.
- The contractor was reminded to provide cover for the rubbish bin for proper storage of general refuse.
- The contractor was reminded to clear the drip tray regularly.
- The contractor was reminded to fix the display screen of the waste water treatment plant.
- The contractor was reminded to provide NRMM label for the generator.
- The contractor was reminded to keep the vehicular access clear.
- The contractor was reminded to clear the stagnant water.
- The contractor was reminded to provide sufficient wheel washing and drainage measures to avoid mud and site runoff carried out by construction vehicles.

H/O Development

- The contractor was reminded to provide covering for the stockpile on site.
- The contractor was reminded to clear the general refuse regularly.
- The contractor was reminded to maintain clearance of mud at site entrance.
- The contractor was reminded to provide covering for the stockpile.

June 2023

KTSP

- The contractor was reminded to clear the stagnant water at the chemical drip tray.
- The contractor was reminded to provide drip tray for chemical container on site.
- The contractor was reminded to clear the stagnant water.
- The contractor was reminded to clear the general refuse regularly.

H/O Development

- The contractor was reminded to display the updated construction noise permit.
- The contractor was reminded to display the chemical waste producer license at the chemical waste storage area.
- The contractor was reminded to keep the vehicle entrance clear from mud.
- The contractor was reminded to provide water spraying for the breaking work.
- The contractor was reminded to provide covered rubbish bin for proper disposal of general refuse.

Review of the effectiveness and efficiency of the EM&A programme will be continued, and recommendations will be provided to remediate any potential impacts due to the project and to improve the EM&A programme if deficiencies of the existing EM&A programme are identified.

4.3 Conclusions

General

The construction works for the Project commenced on 8 April 2019. This is the 17th Quarterly EM&A Report for the Project summarises findings of the EM&A works during the reporting period from 1 April 2023 to 30 June 2023. (the “reporting period”).

Breaches of Action and Limit Levels

Air Quality

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1-T, AMS2 and AMS4 during the reporting period.

Noise

Two noise related complaints were received during the reporting period. Two Action Level exceedances for noise were triggered during the reporting period.

No Limit Level exceedances of noise at NMS1-T, NMS2 and NMS4 was recorded during the reporting period.

Environmental Site Inspections

Environmental site inspections were carried out thirteen times during the reporting period. Recommendations on remedial actions were given to the Contracted Party for the deficiencies identified during the site inspections.


Complaints

There were three complaints received in relation to the environmental impact during the reporting period. Complaint investigations were conducted and mitigation measures were implemented.

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

Figures

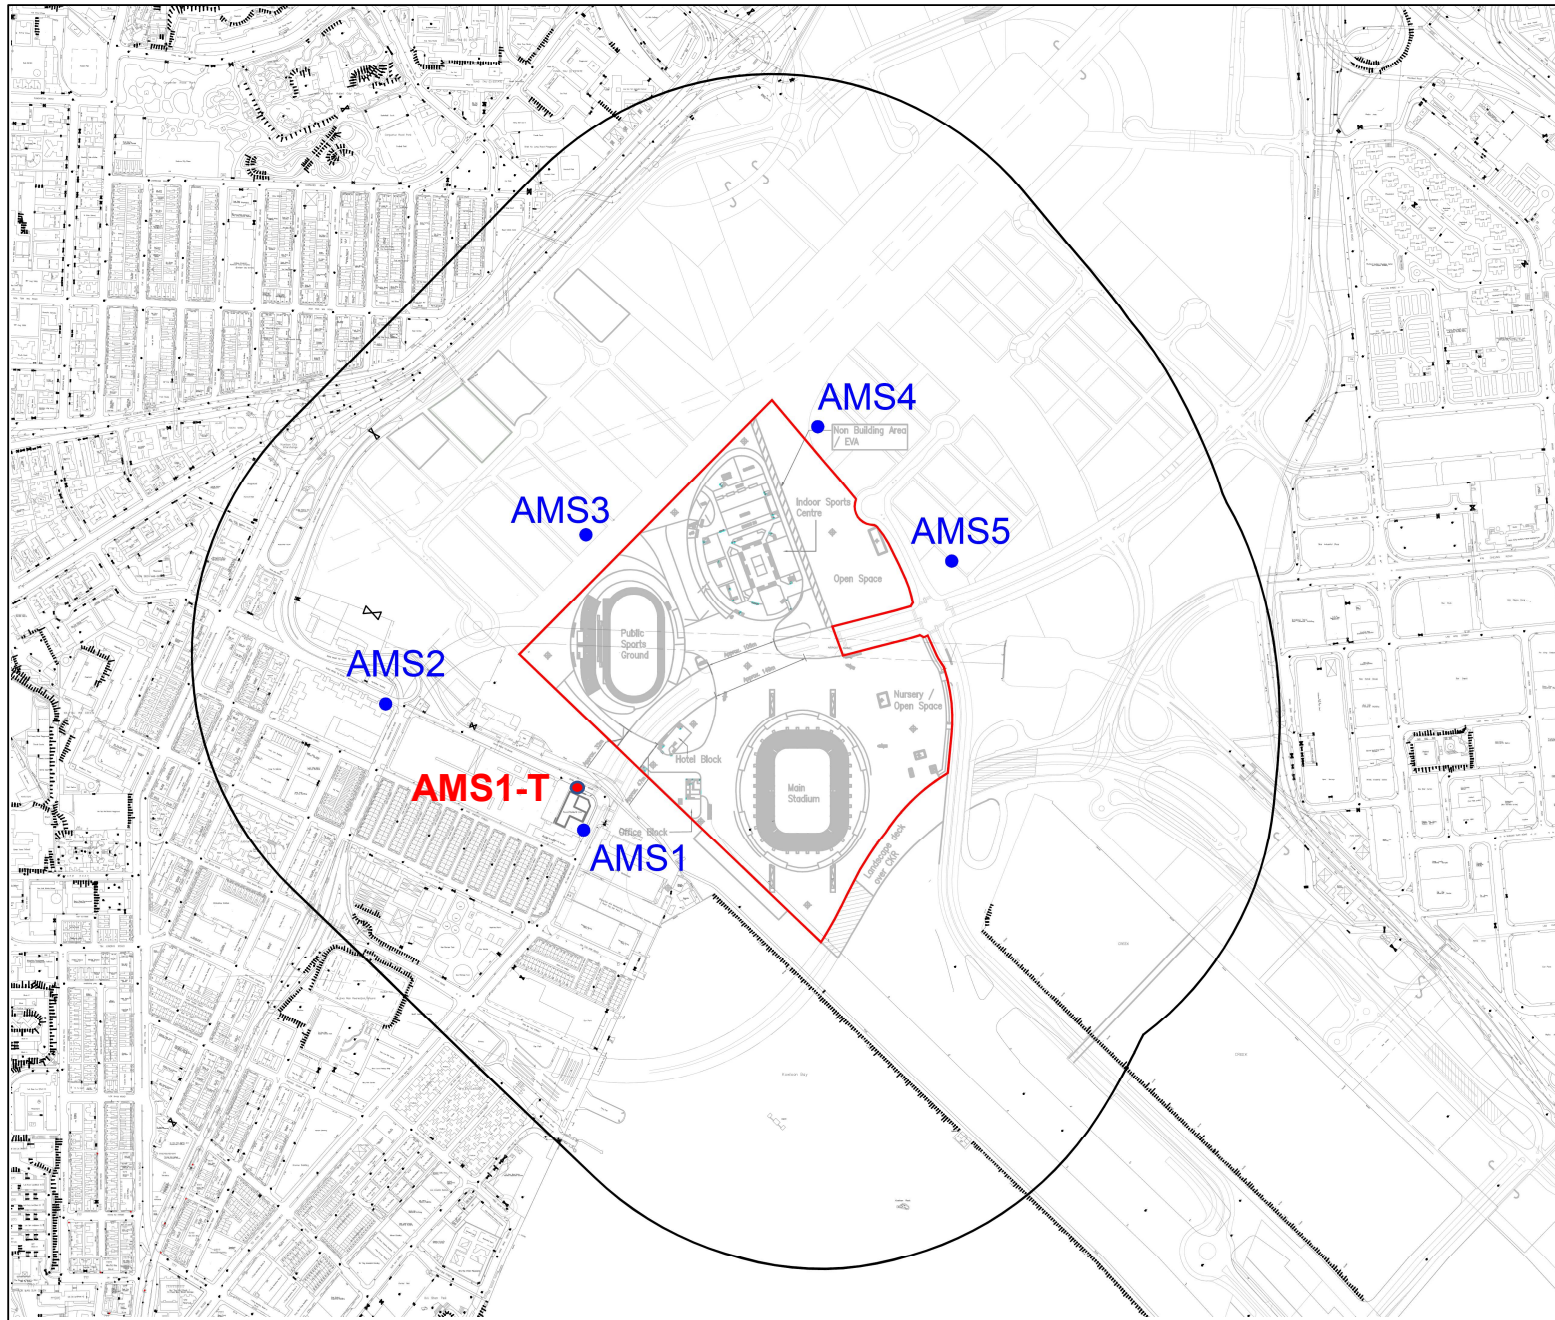

Key Plan

Notes:

1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATES SYSTEM.
3. PIPE AND BOX OR RISE SIZES ARE SHOWN IN MILLIMETERS.

Key to symbols:

LEGEND:

- Project Site
- 500m from Site Boundary
- AMS1 Air Monitoring Station 1
- AMS1-T Temporary Air Monitoring Station

Rev	Date	Drawn	Description	Ch'k'd	App'd

M M

MOTT
MACDONALD

3/F, Maritime Bay Phase
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T: +852 2828 5757
F: +852 2821 1823
W: mottmac.com

Client


Project

Title

**Figure 2.1
Location of Air Quality
Monitoring Stations**

Designed		Eng check	
Drawn		Coordination	
Dwg check		Approved	
Scale at A3	Status		Rev

Drawing Number

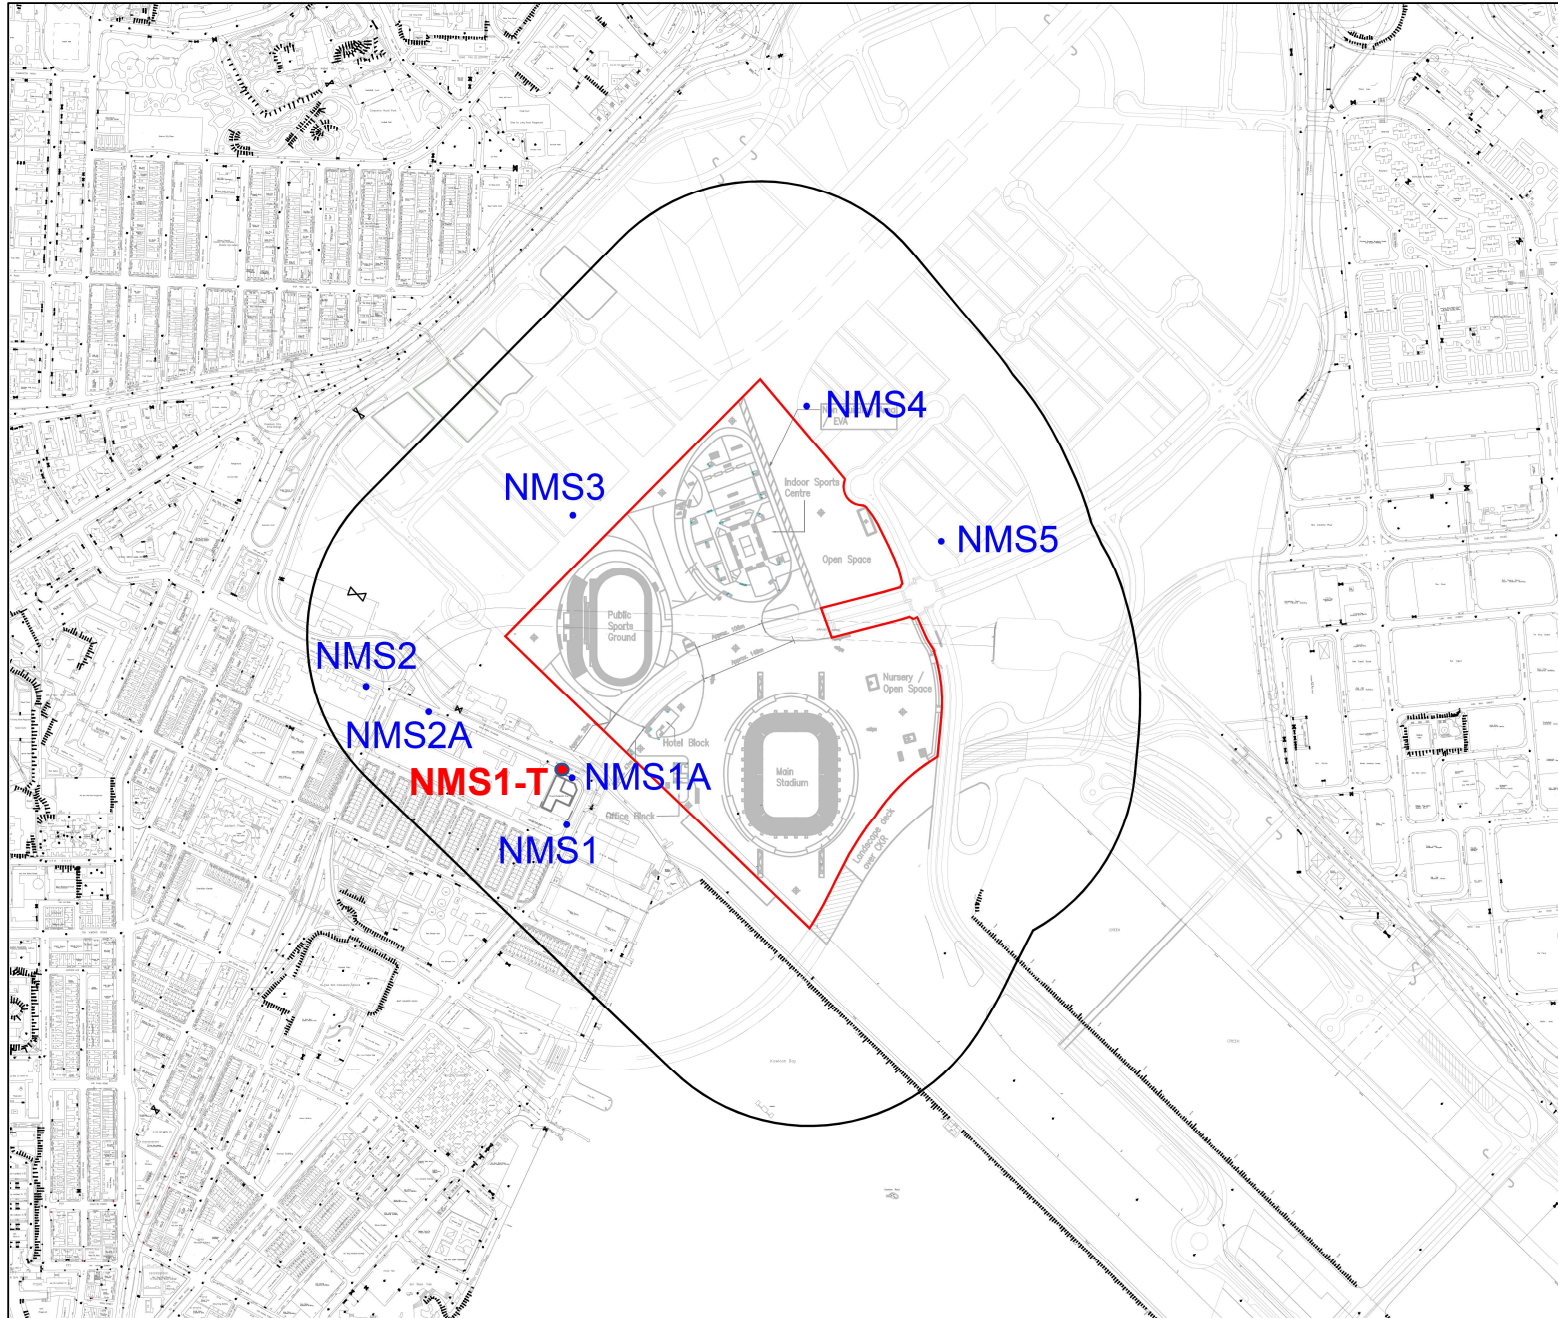

Key Plan

Notes:

1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATES SYSTEM.
3. PIPE AND BOX OR KEY SIZES ARE SHOWN IN MILLIMETERS.

Key to symbols:

LEGEND:

- Project Site
- 300m from Site Boundary
- NMS1 Construction Noise Monitoring Station 1
- NMS1-T Temporary Noise Monitoring Station

Rev	Date	Drawn	Description	Ch'k'd	App'd

M M
MOTT MACDONALD

3/F, Maritime Bay Phase
 348 Kwun Tong Road
 Kwun Tong, Kowloon
 Hong Kong
 T: +852 2828 5757
 F: +852 2821 1823
 W: mottmac.com

Client

Project

Title


Figure 2.2
Location of Noise Monitoring Stations

Designed		Eng check	
Drawn		Co-ordination	
Dwg check		Approved	
Scale at A3	Status		Rev

Drawing Number


Appendix A. Project Organization for Environmental Works

Project Organisation for Environmental Works

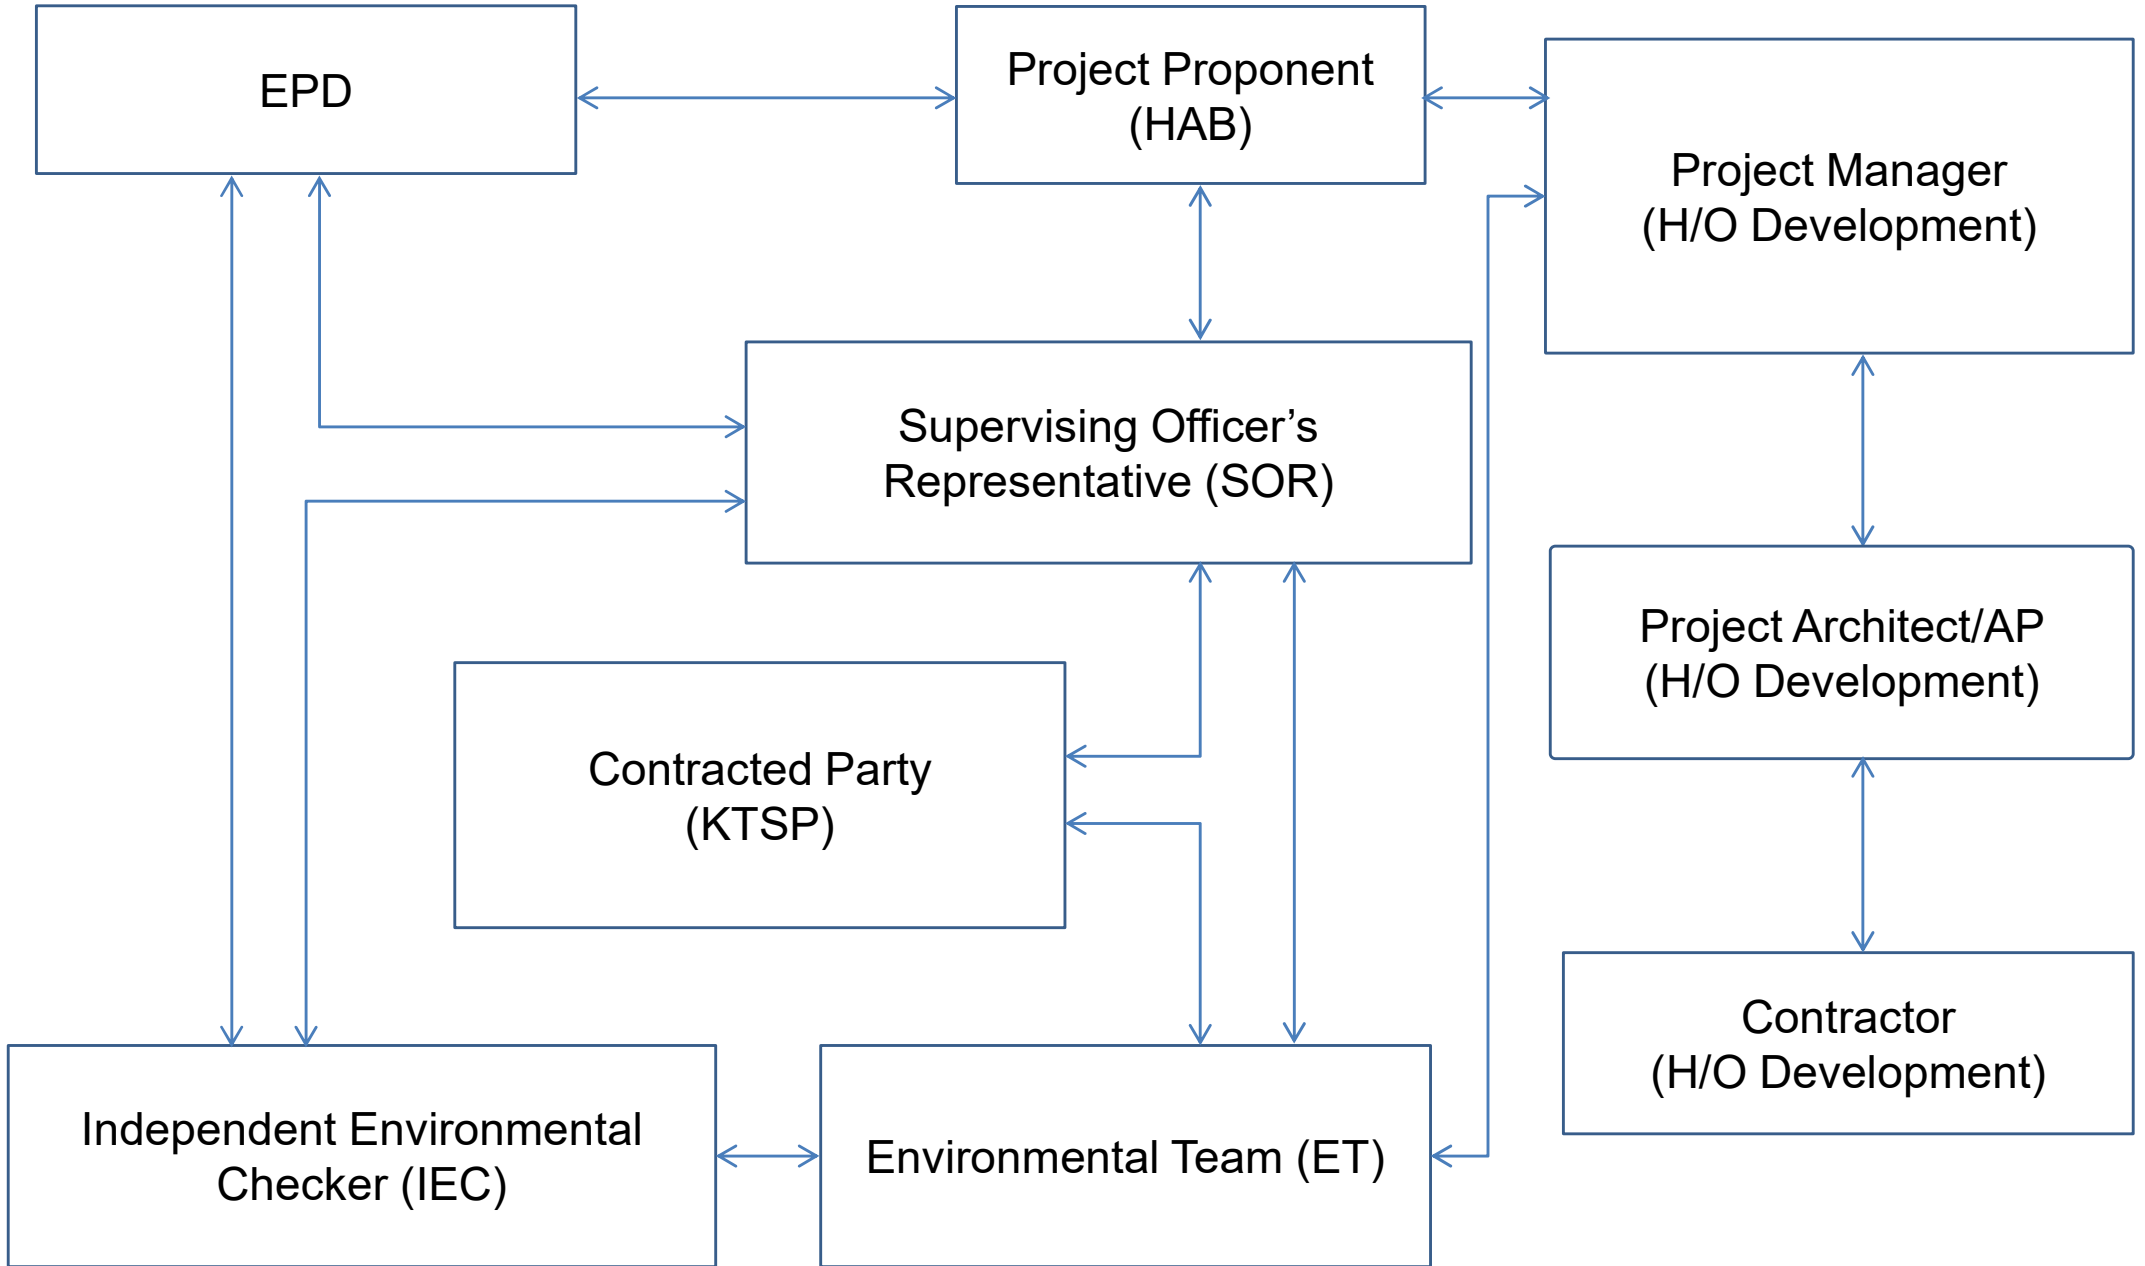

Line of communication

Appendix B. Location of Works Areas

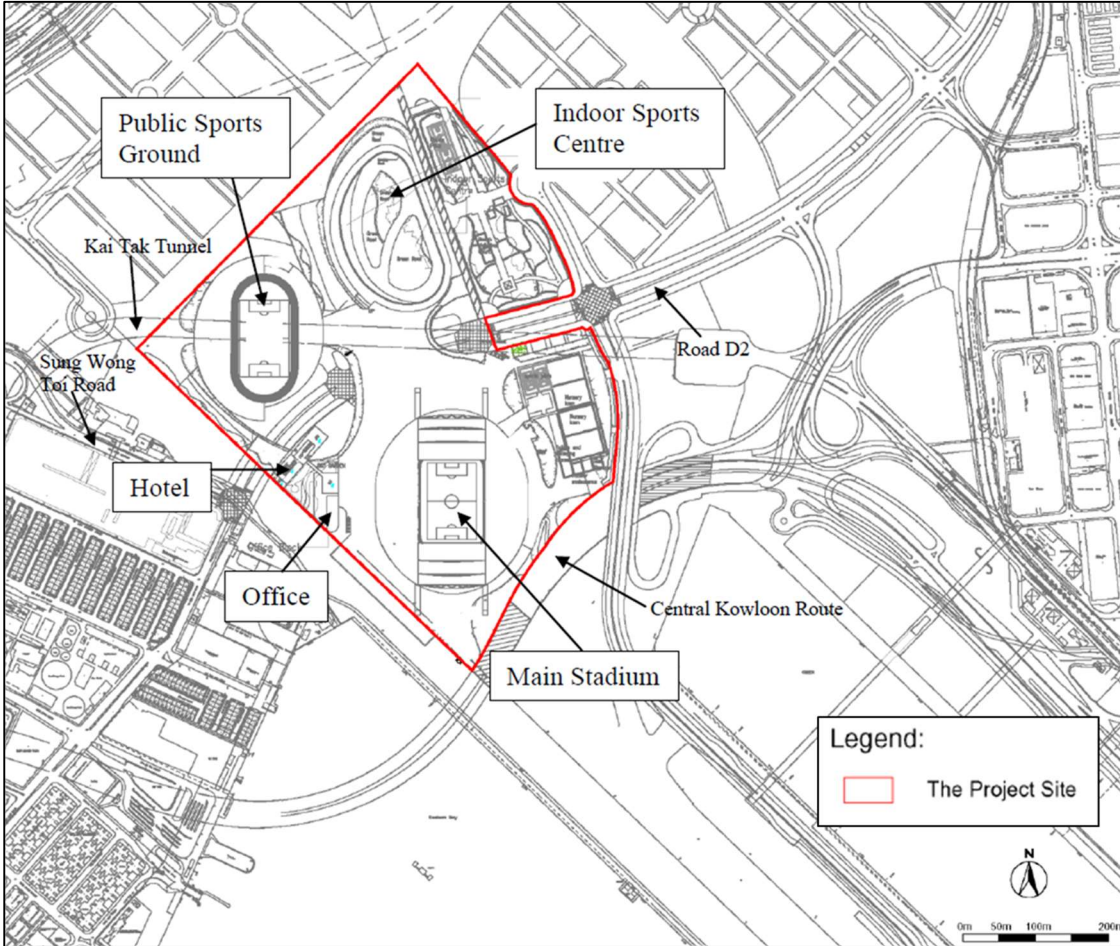

Appendix C. Construction Programme

Appendix D. Event and Action Plan

Should non-compliance of the air quality criteria occur, actions in accordance with the Event and Action Plan in **Table D.1** and **Table D.2** shall be carried out.

Table D.1: Event and Action Plan for Construction Air Quality (Action Level)

Event	Action			
	ET	IEC	SOR	Contracted Party
Action Level				
Exceedance for one sample	1. Inform IEC, SOR and Contracted Party; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Repeat measurement to confirm finding.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method.	1. Notify Contracted Party.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Exceedance for two or more consecutive samples	1. Inform IEC, SOR and Contracted Party; 2. Identify source; 3. Advise the SOR on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC, SOR and Contracted Party on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and SOR; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss with ET and Contracted Party on possible remedial measures; 4. Advise the ET/SOR on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial to SOR and IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

Table D.2: Event and Action Plan for Construction Air Quality (Limit Level)

Event	Action			
	ET	IEC	SOR	Contracted Party
Limit Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Inform IEC, SOR, Contracted Party and EPD; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss with ET and Contracted Party on possible remedial measures; 4. Advise the SOR on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Amend proposal if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, SOR, Contracted Party and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and SOR and Contracted Party to discuss the remedial actions to be taken; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 4. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 5. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. In consultation with the IEC, agree with the Contracted Party on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to SOR and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the SOR until the exceedance ceases.

Should non-compliance of the noise criteria occur, actions in accordance with the Event and Action Plan in **Table D.3** shall be carried out.

Table D.3: Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	SOR	Contracted Party
Action Level	1. Notify IEC, SOR and Contracted Party of exceedance; 2. Identify source; 3. Investigate the causes of exceedance and propose remedial measures; 4. Report the results of investigation to the IEC, SOR and Contracted Party; 5. Discuss with the IEC, SOR and Contracted Party and formulate remedial measures; 6. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contracted Party and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented	1. Submit noise mitigation proposals to SOR with copy to ET and IEC; 2. Implement noise mitigation proposals.
Limit Level	1. Inform IEC, SOR, EPD and Contracted Party; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, SOR and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 2. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented; 5. If exceedance continues, investigate what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to SOR with copy to ET and IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Terminate the relevant portion of works as determined by the SOR until the exceedance ceases.

Appendix E. Monitoring Data and Graphical Plots (Air Quality and Noise)

Data for 1-hour TSP Monitoring at Station AMS1/AMS1-T

	Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ($\mu\text{g}/\text{m}^3$)
*	06-Apr-23	9:02	10:02	Cloudy	0.3	218	39
*	06-Apr-23	10:02	11:02	Cloudy	0.6	161	40
*	06-Apr-23	11:02	12:02	Cloudy	1.4	variable	36
*	11-Apr-23	8:58	9:58	Cloudy	1.1	134	61
*	11-Apr-23	9:58	10:58	Cloudy	2.2	155	69
*	11-Apr-23	10:58	11:58	Cloudy	2.2	168	72
*	17-Apr-23	9:52	10:52	Fine	2.8	147	71
*	17-Apr-23	10:52	11:52	Fine	2.8	155	79
*	17-Apr-23	11:52	12:52	Fine	2.8	126	80
*	21-Apr-23	9:31	10:31	Cloudy	2.5	125	74
*	21-Apr-23	10:31	11:31	Cloudy	2.2	140	88
*	21-Apr-23	11:31	12:31	Cloudy	2.8	111	89
*	27-Apr-23	9:02	10:02	Cloudy	4.7	119	66
*	27-Apr-23	10:02	11:02	Cloudy	4.2	126	59
*	27-Apr-23	11:02	12:02	Cloudy	6.4	116	57
*	03-May-23	9:03	10:03	Cloudy	2.5	119	61
*	03-May-23	10:03	11:03	Cloudy	2.2	129	49
*	03-May-23	11:03	12:03	Cloudy	3.3	108	56
*	09-May-23	8:58	9:58	Cloudy	5.8	119	50
*	09-May-23	9:58	10:58	Cloudy	5.0	115	49
*	09-May-23	10:58	11:58	Cloudy	5.0	114	56
*	15-May-23	9:00	10:00	Cloudy	3.3	134	64
*	15-May-23	10:00	11:00	Cloudy	2.5	110	59
*	15-May-23	11:00	12:00	Cloudy	2.8	139	57
*	19-May-23	8:30	9:30	Cloudy	1.7	154	60
*	19-May-23	9:30	10:30	Cloudy	2.8	153	55
*	19-May-23	10:30	11:30	Cloudy	2.5	149	54
*	24-May-23	9:01	10:01	Cloudy	1.4	variable	74
*	24-May-23	10:01	11:01	Cloudy	3.9	137	71
*	24-May-23	11:01	12:01	Cloudy	3.1	134	68
*	30-May-23	10:26	11:26	Sunny	2.2	147	94
*	30-May-23	11:26	12:26	Sunny	2.8	151	118
*	30-May-23	12:26	13:26	Sunny	2.2	145	124
*	05-Jun-23	9:03	10:03	Fine	6.1	133	49
*	05-Jun-23	10:03	11:03	Fine	5.3	131	57
*	05-Jun-23	11:03	12:03	Fine	5.0	129	58
*	09-Jun-23	8:30	9:30	Cloudy	0.8	145	74
*	09-Jun-23	9:30	10:30	Cloudy	2.2	151	69
*	09-Jun-23	10:30	11:30	Cloudy	0.6	308	67
*	15-Jun-23	9:03	10:03	Cloudy	1.4	151	64
*	15-Jun-23	10:03	11:03	Cloudy	1.1	144	69
*	15-Jun-23	11:03	12:03	Cloudy	1.7	135	72
*	21-Jun-23	9:05	10:05	Fine	2.8	245	59
*	21-Jun-23	10:05	11:05	Fine	3.3	252	62
*	21-Jun-23	11:05	12:05	Fine	3.3	262	55
*	27-Jun-23	9:54	10:54	Fine	2.2	165	51
*	27-Jun-23	10:54	11:54	Fine	2.2	161	49
*	27-Jun-23	11:54	12:54	Fine	3.3	157	48

*Note: During the reporting period, monitoring station AMS1 was no longer open for monitoring from September 2022, due to relocation of the Hong Kong Society for the Blind Workshop. Temporary air quality monitoring station, AMS1-T was used to conduct dust monitoring in September 2022. Details of temporary alternative monitoring locations are presented in Temporary Alternative Proposal for Monitoring Station as proposed by ET and agreed by IEC dated 6 January 2021.

Data for 1-hour TSP Monitoring at Station AMS2

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ($\mu\text{g}/\text{m}^3$)
06-Apr-23	8:18	9:18	Cloudy	1.1	124	36
06-Apr-23	9:18	10:18	Cloudy	0.8	142	42
06-Apr-23	10:18	11:18	Cloudy	1.1	206	38
11-Apr-23	8:15	9:15	Cloudy	2.8	108	51
11-Apr-23	9:15	10:15	Cloudy	1.4	144	56
11-Apr-23	10:15	11:15	Cloudy	2.2	157	60
17-Apr-23	9:06	10:06	Fine	1.1	155	14
17-Apr-23	10:06	11:06	Fine	2.2	151	69
17-Apr-23	11:06	12:06	Fine	3.3	157	75
21-Apr-23	8:20	9:20	Cloudy	3.3	148	84
21-Apr-23	9:20	10:20	Cloudy	2.2	122	91
21-Apr-23	10:20	11:20	Cloudy	2.2	131	96
27-Apr-23	8:18	9:18	Cloudy	4.2	130	65
27-Apr-23	9:18	10:18	Cloudy	5.0	126	49
27-Apr-23	10:18	11:18	Cloudy	4.7	118	47
03-May-23	8:19	9:19	Cloudy	2.2	138	57
03-May-23	9:19	10:19	Cloudy	2.8	128	60
03-May-23	10:19	11:19	Cloudy	1.4	124	49
09-May-23	8:15	9:15	Cloudy	5.3	126	64
09-May-23	9:15	10:15	Cloudy	3.9	134	50
09-May-23	10:15	11:15	Cloudy	5.0	113	48
15-May-23	8:18	9:18	Cloudy	1.7	153	54
15-May-23	9:18	10:18	Cloudy	2.8	132	49
15-May-23	10:18	11:18	Cloudy	3.3	128	52
19-May-23	8:20	9:20	Cloudy	1.7	156	41
19-May-23	9:20	10:20	Cloudy	1.7	149	50
19-May-23	10:20	11:20	Cloudy	2.2	151	44
24-May-23	8:18	9:18	Cloudy	3.1	128	64
24-May-23	9:18	10:18	Cloudy	2.5	142	60
24-May-23	10:18	11:18	Cloudy	2.8	144	55
30-May-23	9:06	10:06	Sunny	0.8	106	101
30-May-23	10:06	11:06	Sunny	1.1	170	114
30-May-23	11:06	12:06	Sunny	3.3	156	121
05-Jun-23	8:20	9:20	Fine	5.3	129	59
05-Jun-23	9:20	10:20	Fine	5.0	127	62
05-Jun-23	10:20	11:20	Fine	5.8	134	69
09-Jun-23	8:20	9:20	Cloudy	0.8	143	74
09-Jun-23	9:20	10:20	Cloudy	1.7	151	71
09-Jun-23	10:20	11:20	Cloudy	0.8	349	61
15-Jun-23	8:20	9:20	Cloudy	0.8	173	44
15-Jun-23	9:20	10:20	Cloudy	1.7	141	54
15-Jun-23	10:20	11:20	Cloudy	1.1	138	50
21-Jun-23	8:22	9:22	Fine	2.2	268	44
21-Jun-23	9:22	10:22	Fine	1.7	248	38
21-Jun-23	10:22	11:22	Fine	3.1	249	51
27-Jun-23	9:02	10:02	Fine	3.3	116	44
27-Jun-23	10:02	11:02	Fine	2.2	165	47
27-Jun-23	11:02	12:02	Fine	2.5	138	42

Data for 1-hour TSP Monitoring at Station AMS4

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ($\mu\text{g}/\text{m}^3$)
06-Apr-23	9:55	10:55	Cloudy	0.6	163	45
06-Apr-23	10:55	11:55	Cloudy	0.8	200	40
06-Apr-23	11:55	12:55	Cloudy	1.7	224	39
11-Apr-23	9:51	10:51	Cloudy	1.7	148	40
11-Apr-23	10:51	11:51	Cloudy	2.2	161	47
11-Apr-23	11:51	12:51	Cloudy	3.3	151	51
17-Apr-23	10:02	11:02	Fine	2.5	153	64
17-Apr-23	11:02	12:02	Fine	3.3	157	66
17-Apr-23	12:02	13:02	Fine	2.2	122	62
21-Apr-23	9:51	10:51	Cloudy	2.8	139	69
21-Apr-23	10:51	11:51	Cloudy	1.7	146	75
21-Apr-23	11:51	12:51	Cloudy	5.0	120	79
27-Apr-23	9:55	10:55	Cloudy	4.7	122	60
27-Apr-23	10:55	11:55	Cloudy	5.6	121	66
27-Apr-23	11:55	12:55	Cloudy	5.8	103	72
03-May-23	9:55	10:55	Cloudy	1.7	146	54
03-May-23	10:55	11:55	Cloudy	3.3	119	50
03-May-23	11:55	12:55	Cloudy	1.9	145	46
09-May-23	9:51	10:51	Cloudy	5.3	116	51
09-May-23	10:51	11:51	Cloudy	5.0	116	48
09-May-23	11:51	12:51	Cloudy	4.4	112	42
15-May-23	9:53	10:53	Cloudy	3.3	118	48
15-May-23	10:53	11:53	Cloudy	3.3	130	47
15-May-23	11:53	12:53	Cloudy	2.2	159	42
19-May-23	8:50	9:50	Cloudy	1.7	136	50
19-May-23	9:50	10:50	Cloudy	2.2	141	46
19-May-23	10:50	11:50	Cloudy	2.5	146	59
24-May-23	9:55	10:55	Cloudy	2.8	142	65
24-May-23	10:55	11:55	Cloudy	2.8	133	75
24-May-23	11:55	12:55	Cloudy	4.7	131	70
30-May-23	11:18	12:18	Sunny	2.2	147	99
30-May-23	12:18	13:18	Sunny	2.2	146	104
30-May-23	13:18	14:18	Sunny	2.2	148	97
05-Jun-23	9:55	10:55	Fine	5.3	131	64
05-Jun-23	10:55	11:55	Fine	4.4	132	59
05-Jun-23	11:55	12:55	Fine	5.0	139	62
09-Jun-23	8:50	9:50	Cloudy	1.4	145	71
09-Jun-23	9:50	10:50	Cloudy	2.5	149	86
09-Jun-23	10:50	11:50	Cloudy	0.3	330	75
15-Jun-23	9:55	10:55	Cloudy	1.7	149	59
15-Jun-23	10:55	11:55	Cloudy	1.4	133	61
15-Jun-23	11:55	12:55	Cloudy	0.3	160	69
21-Jun-23	9:56	10:56	Fine	2.8	252	50
21-Jun-23	10:56	11:56	Fine	2.5	254	42
21-Jun-23	11:56	12:56	Fine	3.3	246	39
27-Jun-23	10:55	11:55	Fine	1.1	175	34
27-Jun-23	11:55	12:55	Fine	2.5	162	29
27-Jun-23	12:55	13:55	Fine	3.3	155	36

Data for Noise Monitoring at Station NMS1/NMS1-T

	Date	Time	Weather	L _{eq} (5min)	L ₁₀	L ₉₀	Measured L _{eq} (30min)
*	06-Apr-23	09:05	Cloudy	71.8	74.0	65.5	
*	06-Apr-23	09:10	Cloudy	70.8	73.1	64.4	
*	06-Apr-23	09:15	Cloudy	71.2	74.3	65.8	
*	06-Apr-23	09:20	Cloudy	71.7	74.6	65.9	71.2
*	06-Apr-23	09:25	Cloudy	70.0	73.9	64.6	
*	06-Apr-23	09:30	Cloudy	71.2	74.4	65.7	
<hr/>							
*	11-Apr-23	09:01	Cloudy	70.5	73.6	62.4	
*	11-Apr-23	09:06	Cloudy	71.7	74.3	63.7	
*	11-Apr-23	09:11	Cloudy	70.8	73.2	62.9	
*	11-Apr-23	09:16	Cloudy	69.6	72.9	62.2	70.4
*	11-Apr-23	09:21	Cloudy	69.1	72.0	62.0	
*	11-Apr-23	09:26	Cloudy	70.3	73.8	63.1	
<hr/>							
*	17-Apr-23	09:55	Fine	70.2	73.5	63.5	
*	17-Apr-23	10:00	Fine	70.9	73.7	63.3	
*	17-Apr-23	10:05	Fine	71.2	73.7	62.9	
*	17-Apr-23	10:10	Fine	70.9	74.2	63.3	70.9
*	17-Apr-23	10:15	Fine	69.9	73.1	64.6	
*	17-Apr-23	10:20	Fine	72.2	75.5	66.7	
<hr/>							
*	27-Apr-23	09:05	Fine	69.5	72.2	64.3	
*	27-Apr-23	09:10	Fine	70.9	73.9	65.4	
*	27-Apr-23	09:15	Fine	70.6	73.5	65.8	
*	27-Apr-23	09:20	Fine	69.1	72.7	64.7	69.9
*	27-Apr-23	09:25	Fine	69.1	72.0	64.2	
*	27-Apr-23	09:30	Fine	70.0	73.4	65.1	
<hr/>							
*	03-May-23	09:06	Cloudy	69.7	72.0	64.3	
*	03-May-23	09:11	Cloudy	70.1	73.2	65.4	
*	03-May-23	09:16	Cloudy	71.9	74.9	65.5	
*	03-May-23	09:21	Cloudy	69.4	72.6	64.8	70.7
*	03-May-23	09:26	Cloudy	71.7	74.6	65.7	
*	03-May-23	09:31	Cloudy	71.0	74.4	65.2	
<hr/>							
*	09-May-23	09:01	Cloudy	70.6	73.2	65.3	
*	09-May-23	09:06	Cloudy	71.8	74.9	66.4	
*	09-May-23	09:11	Cloudy	71.7	74.6	66.5	
*	09-May-23	09:16	Cloudy	70.5	73.8	65.8	71.1
*	09-May-23	09:21	Cloudy	71.1	74.0	66.9	
*	09-May-23	09:26	Cloudy	71.0	74.4	66.3	
<hr/>							
*	15-May-23	09:03	Cloudy	69.9	72.2	64.3	
*	15-May-23	09:08	Cloudy	69.6	72.8	64.4	
*	15-May-23	09:13	Cloudy	70.4	73.6	65.5	
*	15-May-23	09:18	Cloudy	70.7	73.5	65.9	70.5
*	15-May-23	09:23	Cloudy	71.1	74.0	66.4	
*	15-May-23	09:28	Cloudy	71.0	74.1	66.2	
<hr/>							
*	24-May-23	09:04	Cloudy	69.4	72.2	64.3	
*	24-May-23	09:09	Cloudy	70.5	73.6	65.4	
*	24-May-23	09:14	Cloudy	71.6	74.5	66.6	
*	24-May-23	09:19	Cloudy	71.9	74.8	66.7	70.5
*	24-May-23	09:24	Cloudy	70.1	73.0	65.9	
*	24-May-23	09:29	Cloudy	69.0	72.4	64.1	
<hr/>							
*	30-May-23	09:54	Sunny	72.1	75.7	63.1	
*	30-May-23	09:59	Sunny	71.6	74.9	63.8	
*	30-May-23	10:04	Sunny	72.4	76.3	62.5	
*	30-May-23	10:09	Sunny	69.8	73.0	63.3	72.1
*	30-May-23	10:14	Sunny	71.5	75.3	65.3	
*	30-May-23	10:19	Sunny	74.2	78.6	62.0	

	Date	Time	Weather	L _{eq} (5min)	L ₁₀	L ₉₀	Measured L _{eq} (30min)
*	05-Jun-23	09:06	Fine	70.0	73.1	65.2	
*	05-Jun-23	09:11	Fine	69.4	72.2	64.3	
*	05-Jun-23	09:16	Fine	69.1	72.9	64.4	
*	05-Jun-23	09:21	Fine	71.6	73.5	65.6	70.6
*	05-Jun-23	09:26	Fine	71.8	73.7	65.9	
*	05-Jun-23	09:31	Fine	70.7	73.6	65.8	
*	15-Jun-23	09:06	Cloudy	70.4	73.6	65.7	
*	15-Jun-23	09:11	Cloudy	69.6	72.8	64.5	
*	15-Jun-23	09:16	Cloudy	69.9	72.4	64.2	
*	15-Jun-23	09:21	Cloudy	70.3	73.2	65.9	70.1
*	15-Jun-23	09:26	Cloudy	69.1	72.0	64.6	
*	15-Jun-23	09:31	Cloudy	71.0	74.7	65.0	
*	21-Jun-23	09:08	Fine	69.0	72.1	64.2	
*	21-Jun-23	09:13	Fine	69.9	72.7	64.3	
*	21-Jun-23	09:18	Fine	70.4	73.4	65.5	
*	21-Jun-23	09:23	Fine	70.1	73.6	65.9	70.5
*	21-Jun-23	09:28	Fine	71.7	74.8	65.8	
*	21-Jun-23	09:33	Fine	71.5	74.6	66.2	
*	27-Jun-23	09:57	Fine	73.3	76.9	62.8	
*	27-Jun-23	10:02	Fine	72.7	76.0	63.5	
*	27-Jun-23	10:07	Fine	71.6	74.9	63.1	
*	27-Jun-23	10:12	Fine	72.7	77.0	62.5	72.3
*	27-Jun-23	10:17	Fine	71.6	73.8	63.0	
*	27-Jun-23	10:22	Fine	71.4	75.1	62.0	

*** Note:**

During the reporting period, monitoring station NMS1 was no longer open for impact monitoring from September 2022, due to relocation of the Hong Kong Society for the Blind Workshop. Temporary noise monitoring station, NMS1-T was used to conduct noise monitoring in September 2022. Details of temporary alternative monitoring locations are presented in Temporary Alternative Proposal for Monitoring Station as proposed by ET and agreed by IEC dated 6 January 2021.

Data for Noise Monitoring at Station NMS2

Date	Time	Weather	L _{eq} (5min)	L ₁₀	L ₉₀	Measured L _{eq} (30min)
06-Apr-23	08:21	Cloudy	68.7	70.0	66.6	
06-Apr-23	08:26	Cloudy	69.3	71.1	67.4	
06-Apr-23	08:31	Cloudy	70.2	72.5	68.6	69.8
06-Apr-23	08:36	Cloudy	70.9	72.9	68.8	
06-Apr-23	08:41	Cloudy	69.4	71.8	67.9	
06-Apr-23	08:46	Cloudy	70.1	72.4	68.2	
11-Apr-23	08:18	Cloudy	68.5	70.2	64.3	
11-Apr-23	08:23	Cloudy	69.7	71.8	65.4	
11-Apr-23	08:28	Cloudy	68.6	70.5	64.9	69.0
11-Apr-23	08:33	Cloudy	69.3	71.7	65.7	
11-Apr-23	08:38	Cloudy	68.1	70.0	64.4	
11-Apr-23	08:43	Cloudy	69.4	71.9	65.2	
17-Apr-23	09:09	Fine	68.5	71.9	63.2	
17-Apr-23	09:14	Fine	68.3	70.6	63.3	
17-Apr-23	09:19	Fine	68.3	71.6	62.4	69.2
17-Apr-23	09:24	Fine	69.3	71.6	65.3	
17-Apr-23	09:29	Fine	69.6	72.1	64.0	
17-Apr-23	09:34	Fine	70.6	72.7	66.8	
27-Apr-23	08:21	Fine	67.9	69.2	65.3	
27-Apr-23	08:26	Fine	68.7	70.8	66.4	
27-Apr-23	08:31	Fine	68.6	70.5	66.9	68.7
27-Apr-23	08:36	Fine	69.4	71.4	67.6	
27-Apr-23	08:41	Fine	69.1	71.0	67.5	
27-Apr-23	08:46	Fine	68.3	70.1	66.2	
03-May-23	08:22	Cloudy	67.4	69.2	65.3	
03-May-23	08:27	Cloudy	68.1	70.6	66.4	
03-May-23	08:32	Cloudy	69.9	71.5	67.8	68.1
03-May-23	08:37	Cloudy	67.6	69.7	65.6	
03-May-23	08:42	Cloudy	68.1	70.0	66.5	
03-May-23	08:47	Cloudy	67.2	69.9	65.2	
09-May-23	08:18	Cloudy	69.4	71.2	67.3	
09-May-23	08:23	Cloudy	68.5	70.5	66.4	
09-May-23	08:28	Cloudy	68.6	70.7	66.8	69.2
09-May-23	08:33	Cloudy	70.9	72.6	68.7	
09-May-23	08:38	Cloudy	69.1	71.0	67.6	
09-May-23	08:43	Cloudy	68.0	70.9	66.5	
15-May-23	08:21	Cloudy	68.8	70.2	64.3	
15-May-23	08:26	Cloudy	69.4	71.9	65.4	
15-May-23	08:31	Cloudy	68.9	70.5	64.8	69.3
15-May-23	08:36	Cloudy	68.6	70.7	64.6	
15-May-23	08:41	Cloudy	69.1	71.0	65.4	
15-May-23	08:46	Cloudy	70.5	72.2	65.0	
24-May-23	08:21	Cloudy	68.9	70.0	66.2	
24-May-23	08:26	Cloudy	68.7	70.1	66.4	
24-May-23	08:31	Cloudy	69.2	71.3	67.5	69.9
24-May-23	08:36	Cloudy	70.4	72.6	68.9	
24-May-23	08:41	Cloudy	70.7	72.8	68.7	
24-May-23	08:46	Cloudy	71.0	73.5	69.0	
30-May-23	09:09	Sunny	68.8	71.4	64.3	
30-May-23	09:14	Sunny	68.7	71.6	64.6	
30-May-23	09:19	Sunny	68.6	70.6	63.6	68.8
30-May-23	09:24	Sunny	68.4	71.1	63.9	
30-May-23	09:29	Sunny	69.2	71.6	65.7	
30-May-23	09:34	Sunny	69.2	72.3	64.6	

Date	Time	Weather	L _{eq} (5min)	L ₁₀	L ₉₀	Measured L _{eq} (30min)
05-Jun-23	08:23	Fine	68.4	70.6	66.4	
05-Jun-23	08:28	Fine	68.5	70.5	66.3	
05-Jun-23	08:33	Fine	69.6	71.2	67.7	69.5
05-Jun-23	08:38	Fine	70.9	72.8	68.1	
05-Jun-23	08:43	Fine	70.1	72.0	68.9	
05-Jun-23	08:48	Fine	69.0	71.3	67.2	
15-Jun-23	08:23	Cloudy	69.1	71.0	67.2	
15-Jun-23	08:28	Cloudy	68.9	70.3	66.4	
15-Jun-23	08:33	Cloudy	69.7	71.5	67.8	69.8
15-Jun-23	08:38	Cloudy	70.6	72.7	67.7	
15-Jun-23	08:43	Cloudy	70.1	72.9	68.1	
15-Jun-23	08:48	Cloudy	69.9	71.6	67.6	
21-Jun-23	08:25	Fine	68.5	70.6	66.7	
21-Jun-23	08:30	Fine	69.4	71.3	67.6	
21-Jun-23	08:35	Fine	68.9	70.2	66.9	69.1
21-Jun-23	08:40	Fine	68.1	70.8	66.2	
21-Jun-23	08:45	Fine	69.0	71.7	67.6	
21-Jun-23	08:50	Fine	70.2	72.1	68.0	
27-Jun-23	09:05	Fine	69.1	71.7	64.4	
27-Jun-23	09:10	Fine	69.3	72.0	65.1	
27-Jun-23	09:15	Fine	68.7	71.1	65.4	69.5
27-Jun-23	09:20	Fine	70.6	73.7	66.1	
27-Jun-23	09:25	Fine	69.1	71.4	65.6	
27-Jun-23	09:30	Fine	70.0	72.7	66.2	



Data for Noise Monitoring at Station NMS4

Date	Time	Weather	Leq(5min)	L10	L90	Measured Leq(30min)
06-Apr-23	08:21	Cloudy	64.6	66.4	62.6	
06-Apr-23	08:26	Cloudy	63.9	65.5	61.3	
06-Apr-23	08:31	Cloudy	63.7	65.8	61.2	64.2
06-Apr-23	08:36	Cloudy	64.5	66.7	62.9	
06-Apr-23	08:41	Cloudy	63.4	65.1	61.7	
06-Apr-23	08:46	Cloudy	65.0	67.5	63.4	
11-Apr-23	08:18	Cloudy	63.7	65.2	61.3	
11-Apr-23	08:23	Cloudy	64.7	66.8	62.4	
11-Apr-23	08:28	Cloudy	63.6	65.5	61.9	63.8
11-Apr-23	08:33	Cloudy	64.1	66.0	62.7	
11-Apr-23	08:38	Cloudy	63.5	65.6	61.4	
11-Apr-23	08:43	Cloudy	63.2	65.7	61.3	
17-Apr-23	09:09	Fine	66.5	69.5	62.7	
17-Apr-23	09:14	Fine	69.8	73.2	63.3	
17-Apr-23	09:19	Fine	69.3	72.3	63.7	67.5
17-Apr-23	09:24	Fine	67.0	70.4	61.3	
17-Apr-23	09:29	Fine	66.5	68.9	61.1	
17-Apr-23	09:34	Fine	62.2	64.6	59.4	
27-Apr-23	08:21	Cloudy	64.1	66.2	62.3	
27-Apr-23	08:26	Cloudy	65.4	67.9	63.4	
27-Apr-23	08:31	Cloudy	63.6	65.5	61.8	64.8
27-Apr-23	08:36	Cloudy	64.9	66.7	62.7	
27-Apr-23	08:41	Cloudy	65.1	67.0	63.5	
27-Apr-23	08:46	Cloudy	65.3	67.8	63.2	
03-May-23	08:22	Cloudy	64.4	66.2	62.3	
03-May-23	08:27	Cloudy	63.1	65.7	61.4	
03-May-23	08:32	Cloudy	63.2	65.6	61.5	63.8
03-May-23	08:37	Cloudy	64.7	66.8	62.9	
03-May-23	08:42	Cloudy	64.1	66.0	62.6	
03-May-23	08:47	Cloudy	62.9	64.3	60.2	
09-May-23	08:18	Cloudy	64.9	66.2	62.3	
09-May-23	08:23	Cloudy	65.6	67.3	63.4	
09-May-23	08:28	Cloudy	64.7	66.6	62.5	64.6
09-May-23	08:33	Cloudy	65.5	67.8	63.9	
09-May-23	08:38	Cloudy	63.1	65.0	61.6	
09-May-23	08:43	Cloudy	63.4	65.7	61.4	
15-May-23	08:21	Cloudy	64.7	66.3	62.4	
15-May-23	08:26	Cloudy	63.4	65.2	61.5	
15-May-23	08:31	Cloudy	64.8	66.7	62.6	64.3
15-May-23	08:36	Cloudy	65.2	67.3	63.9	
15-May-23	08:41	Cloudy	63.1	65.0	61.8	
15-May-23	08:46	Cloudy	64.0	66.9	62.4	
24-May-23	08:21	Cloudy	64.4	66.2	62.3	
24-May-23	08:26	Cloudy	63.1	65.6	61.4	
24-May-23	08:31	Cloudy	64.2	66.5	62.6	64.2
24-May-23	08:36	Cloudy	63.8	65.7	61.9	
24-May-23	08:41	Cloudy	65.1	67.0	63.4	
24-May-23	08:46	Cloudy	64.5	66.9	62.0	
30-May-23	09:09	Sunny	72.3	75.9	65.7	
30-May-23	09:14	Sunny	70.9	75.2	65.1	
30-May-23	09:19	Sunny	70.6	74.6	65.6	70.0
30-May-23	09:24	Sunny	70.4	74.2	63.8	
30-May-23	09:29	Sunny	66.1	69.0	61.7	
30-May-23	09:34	Sunny	65.7	68.5	62.0	



Date	Time	Weather	L _{eq} (5min)	L ₁₀	L ₉₀	Measured L _{eq} (30min)
05-Jun-23	08:23	Fine	63.5	65.4	61.5	63.8
05-Jun-23	08:28	Fine	62.9	64.6	60.3	
05-Jun-23	08:33	Fine	64.7	66.2	62.8	
05-Jun-23	08:38	Fine	64.1	66.9	62.4	
05-Jun-23	08:43	Fine	63.1	65.0	61.5	
05-Jun-23	08:48	Fine	64.0	66.7	62.2	
15-Jun-23	08:23	Cloudy	65.0	67.1	63.2	64.7
15-Jun-23	08:28	Cloudy	64.4	66.3	62.4	
15-Jun-23	08:33	Cloudy	63.9	65.5	61.8	
15-Jun-23	08:38	Cloudy	64.6	66.7	62.7	
15-Jun-23	08:43	Cloudy	64.7	66.9	62.1	
15-Jun-23	08:48	Cloudy	65.2	67.0	63.6	
21-Jun-23	08:25	Fine	63.4	65.9	61.8	64.4
21-Jun-23	08:30	Fine	64.6	66.7	62.1	
21-Jun-23	08:35	Fine	65.5	67.4	63.6	
21-Jun-23	08:40	Fine	64.3	66.2	62.4	
21-Jun-23	08:45	Fine	64.1	66.0	62.7	
21-Jun-23	08:50	Fine	63.9	65.2	61.1	
27-Jun-23	09:05	Fine	64.8	66.7	62.5	64.8
27-Jun-23	09:10	Fine	66.6	67.0	63.0	
27-Jun-23	09:15	Fine	64.1	66.5	61.4	
27-Jun-23	09:20	Fine	63.3	65.3	61.0	
27-Jun-23	09:25	Fine	64.1	66.3	61.6	
27-Jun-23	09:30	Fine	65.1	67.4	61.7	

Appendix F. Wind Data



6 April 2023

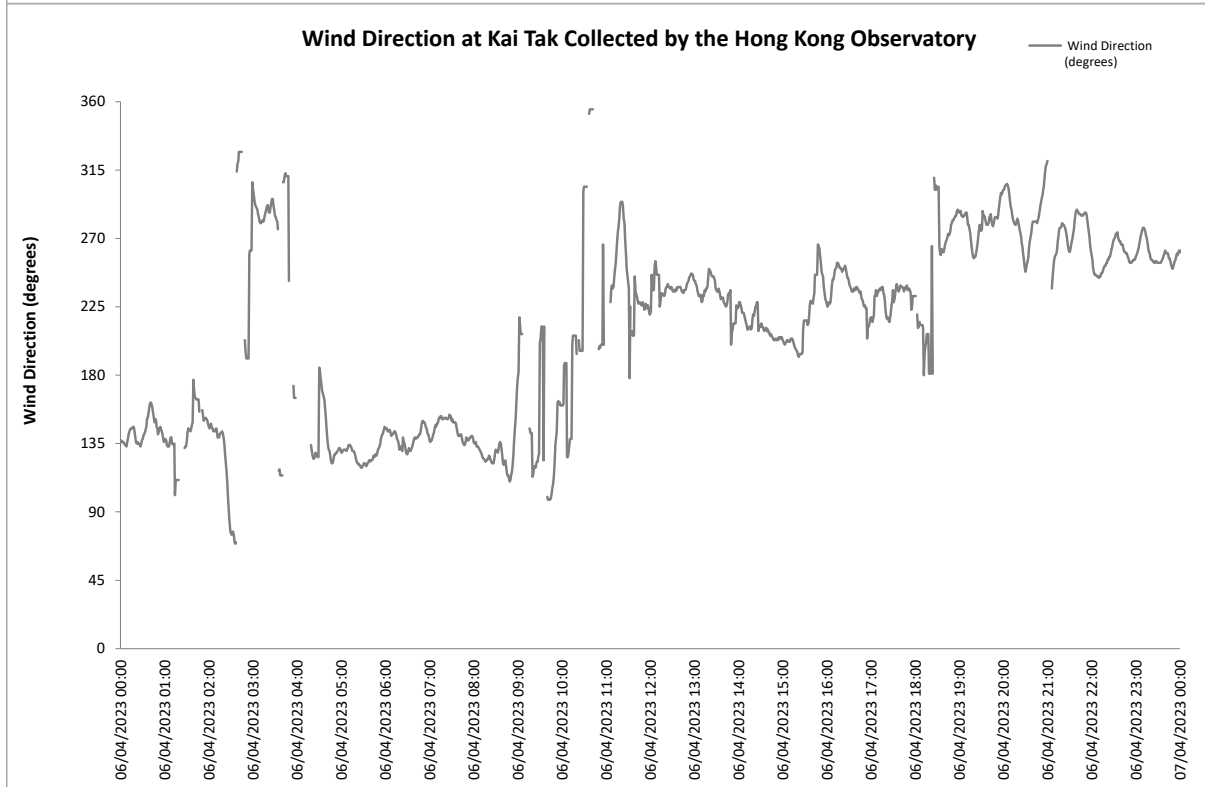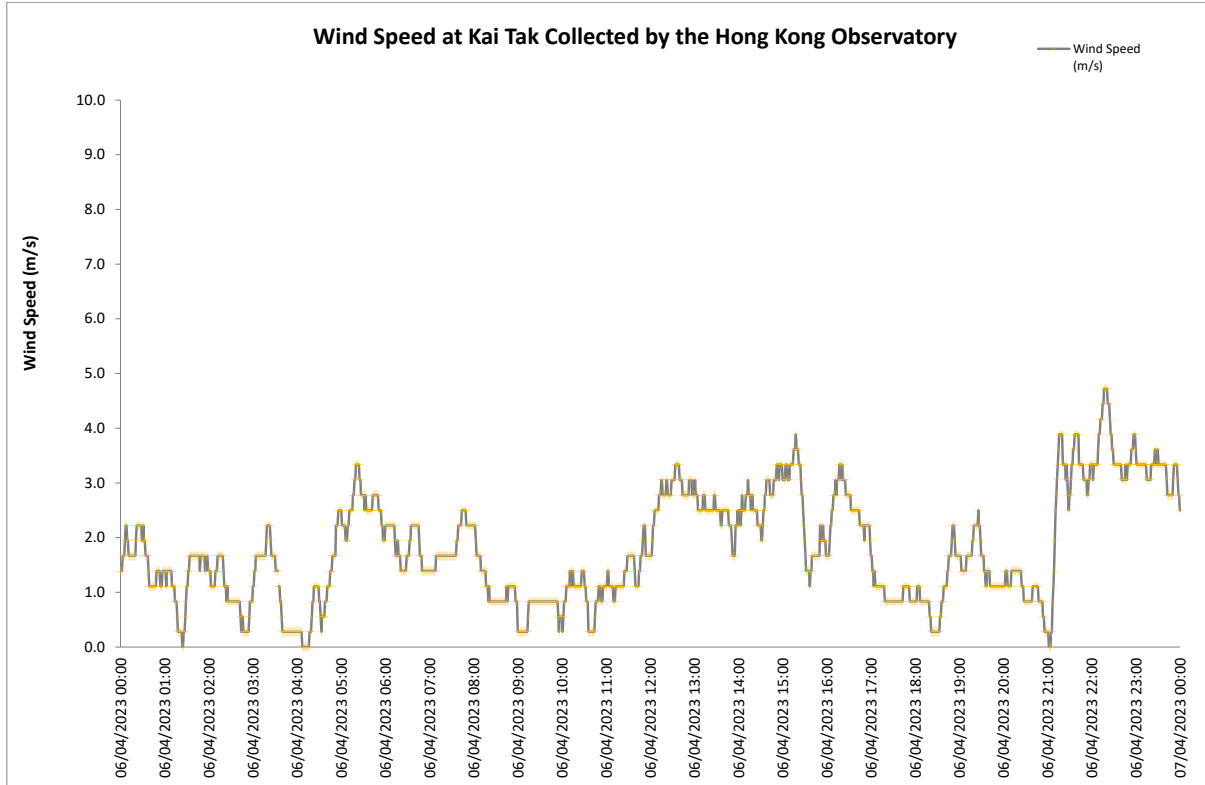



11 April 2023

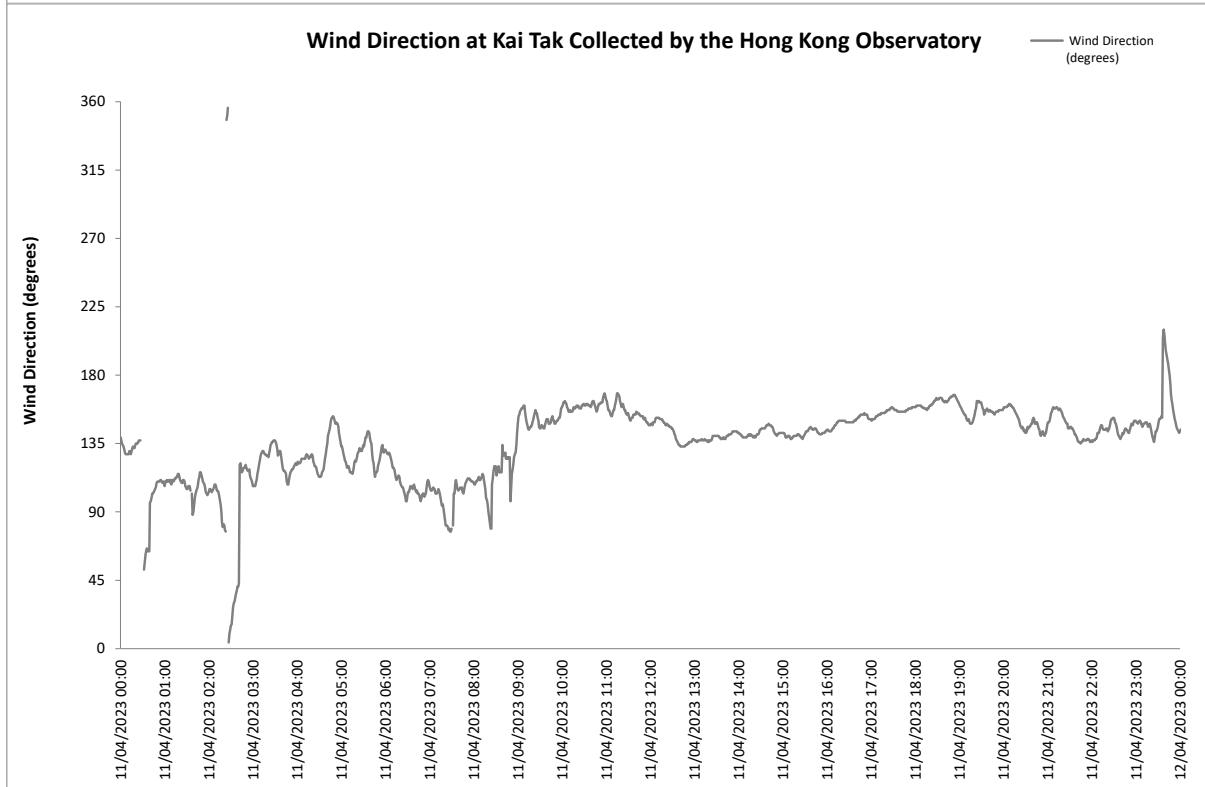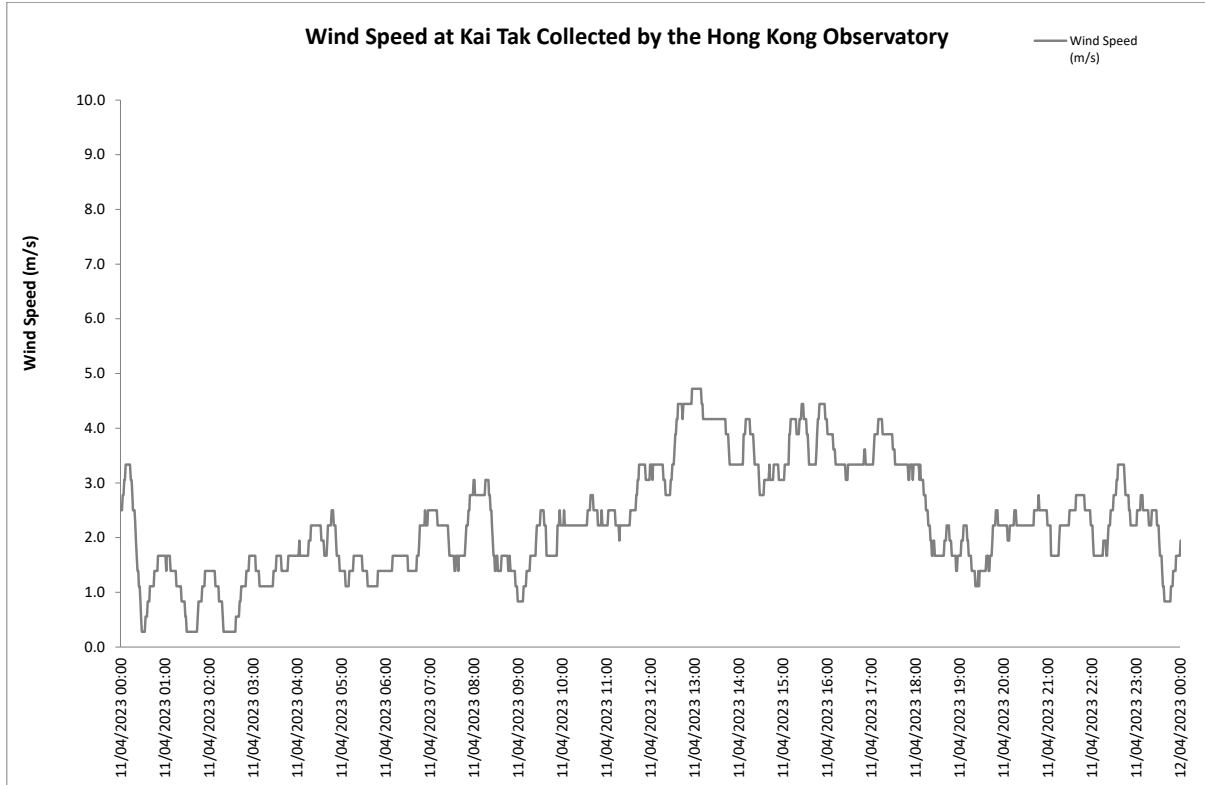



17 April 2023

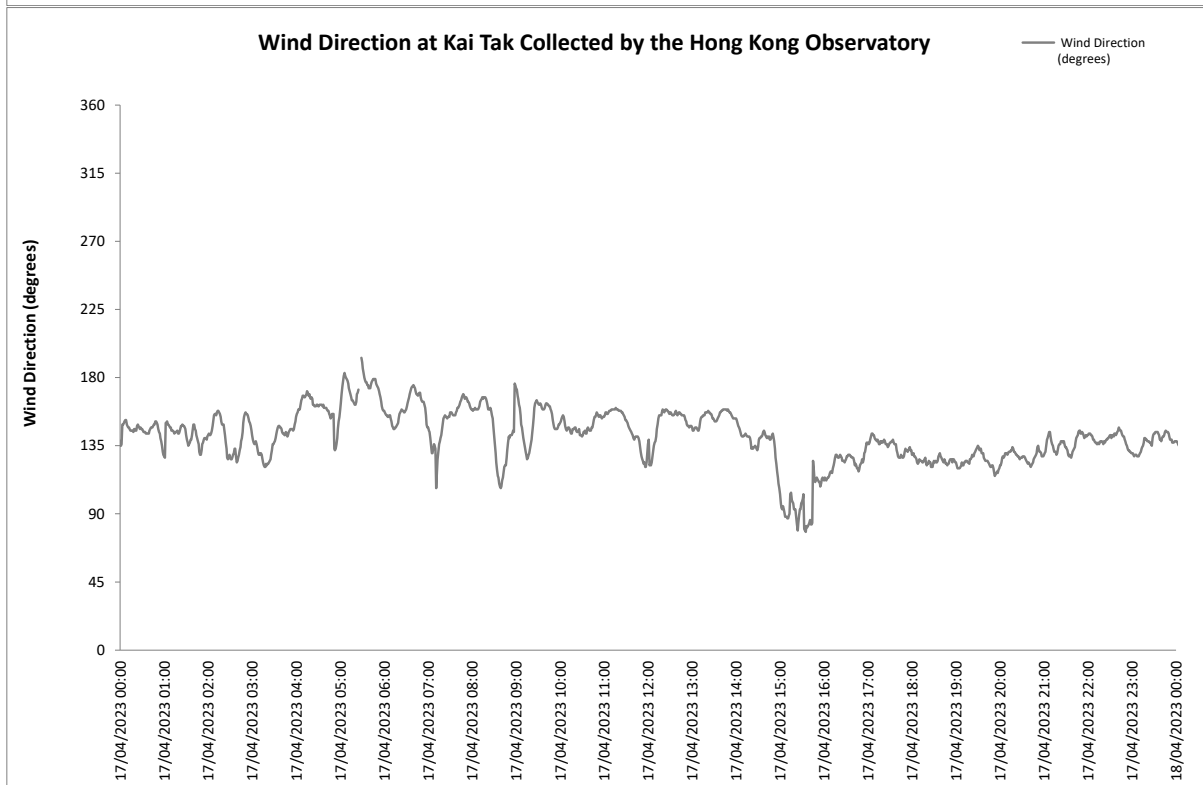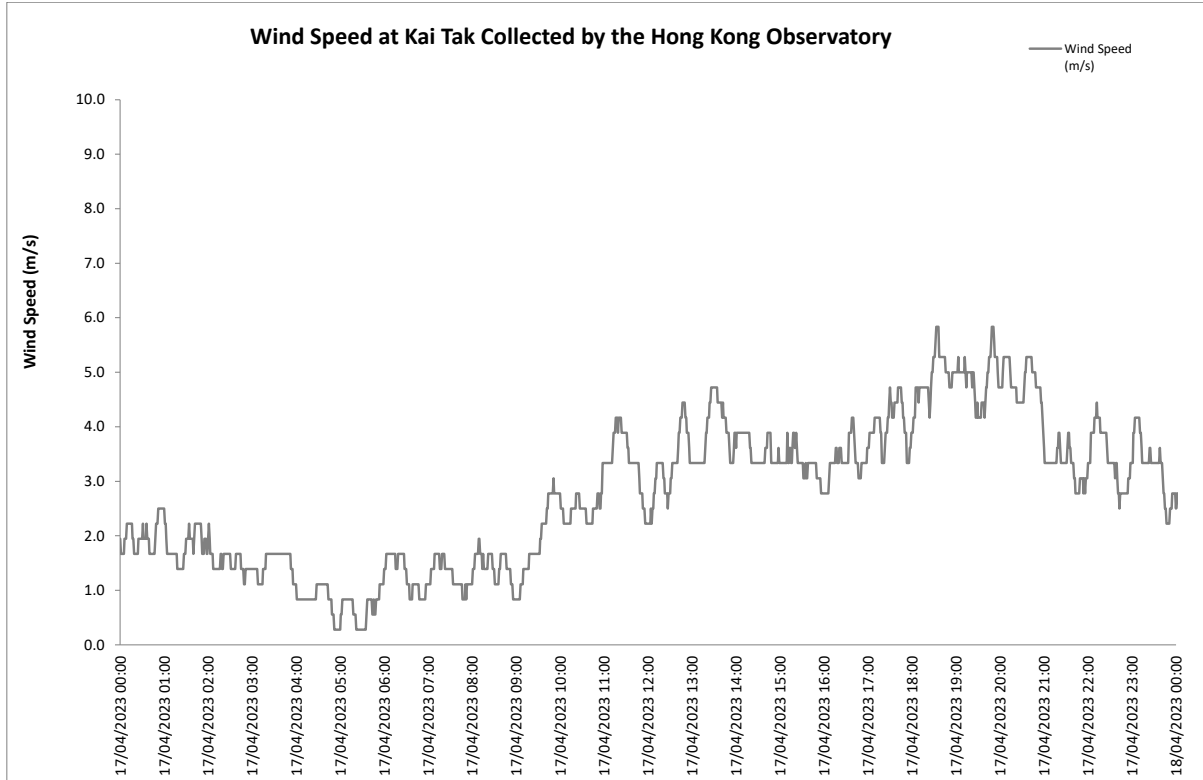



21 April 2023

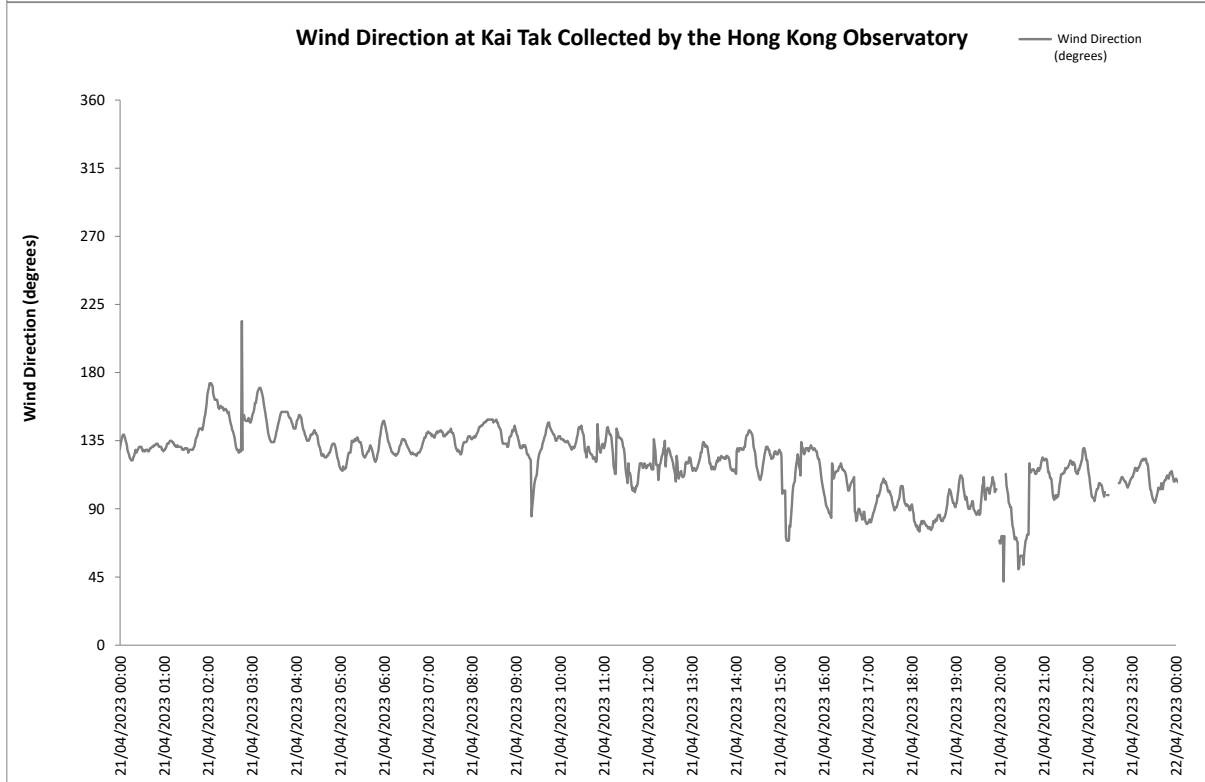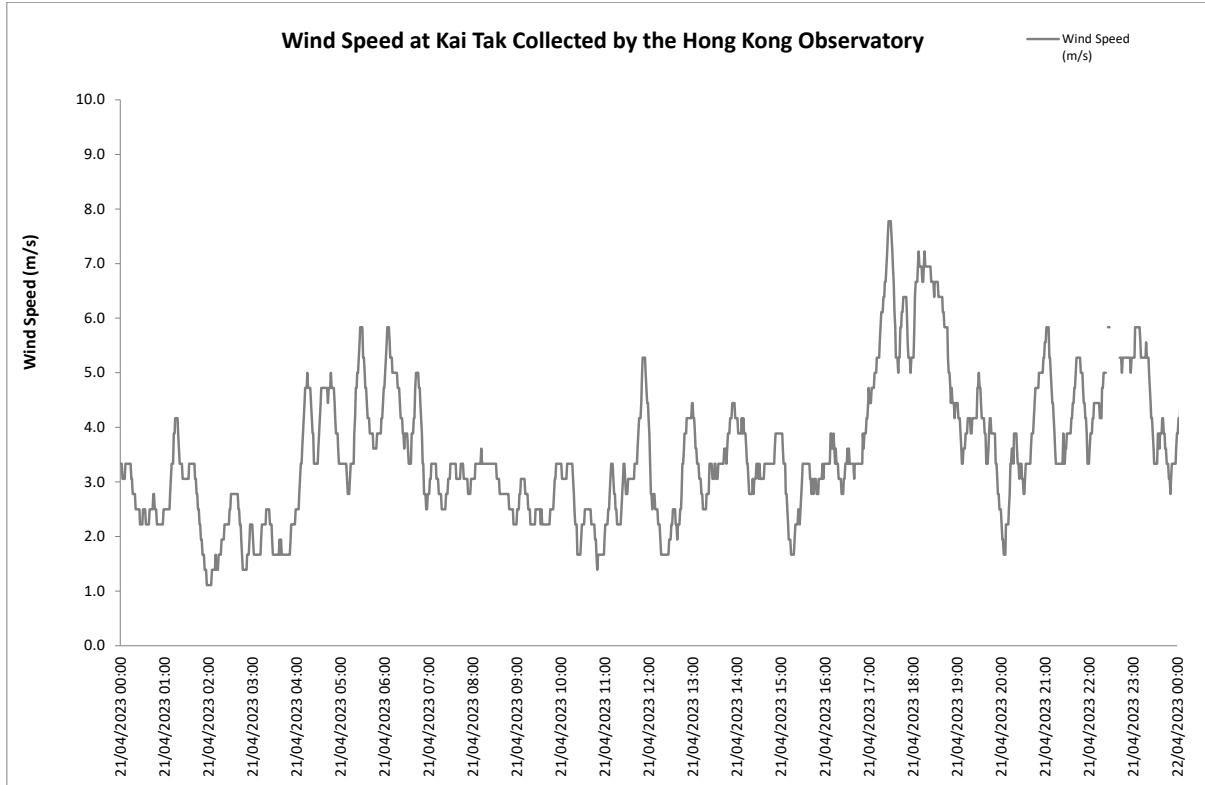



27 April 2023

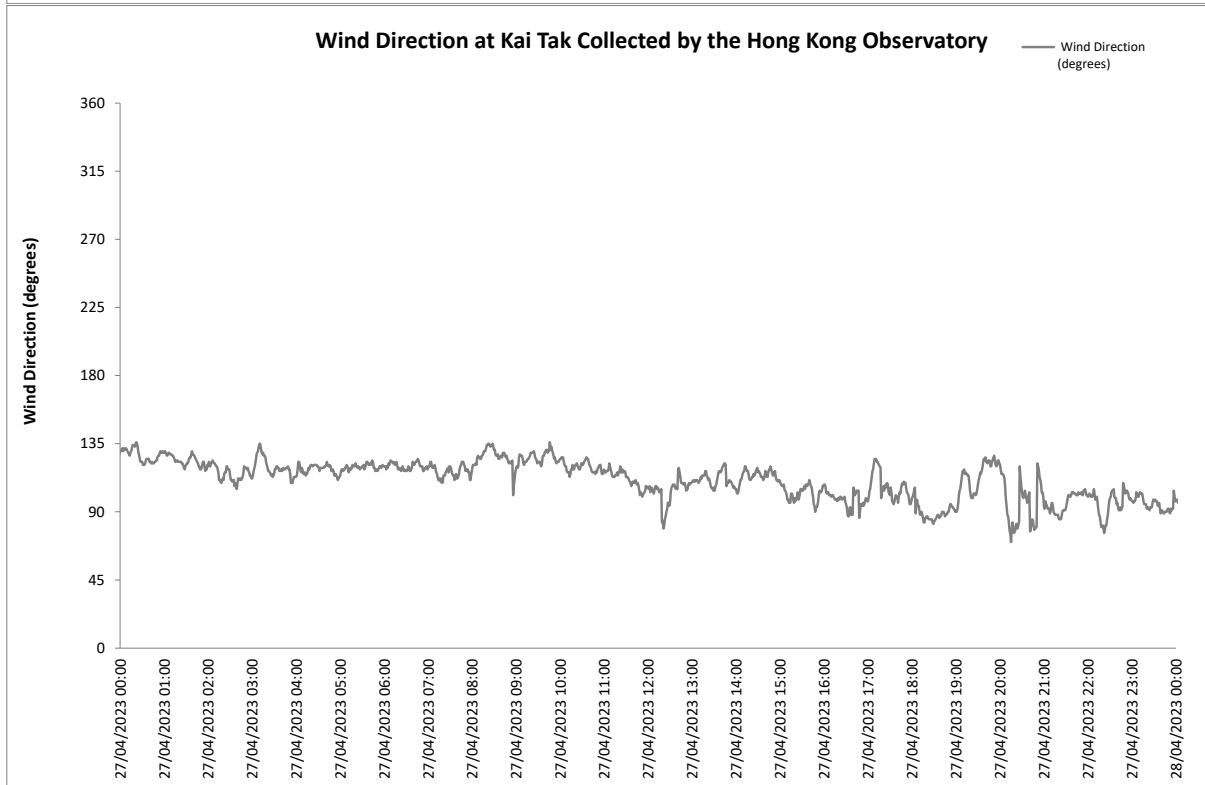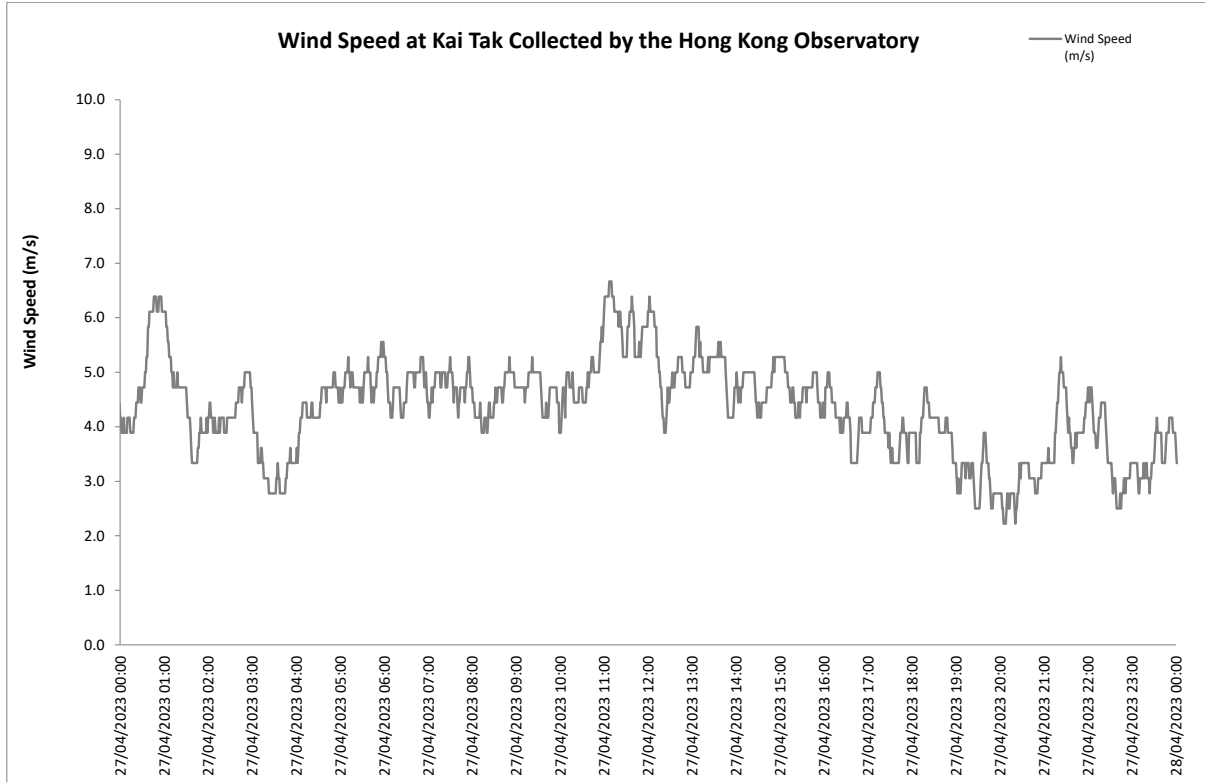



3 May 2023

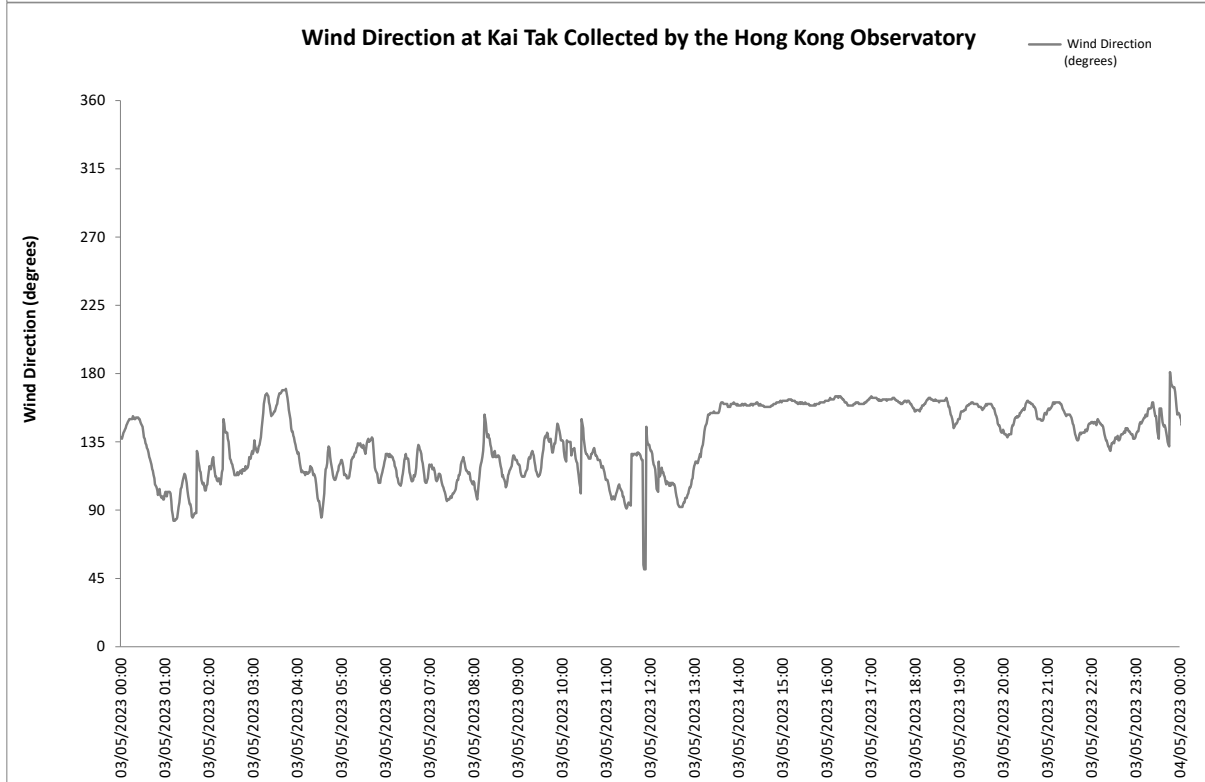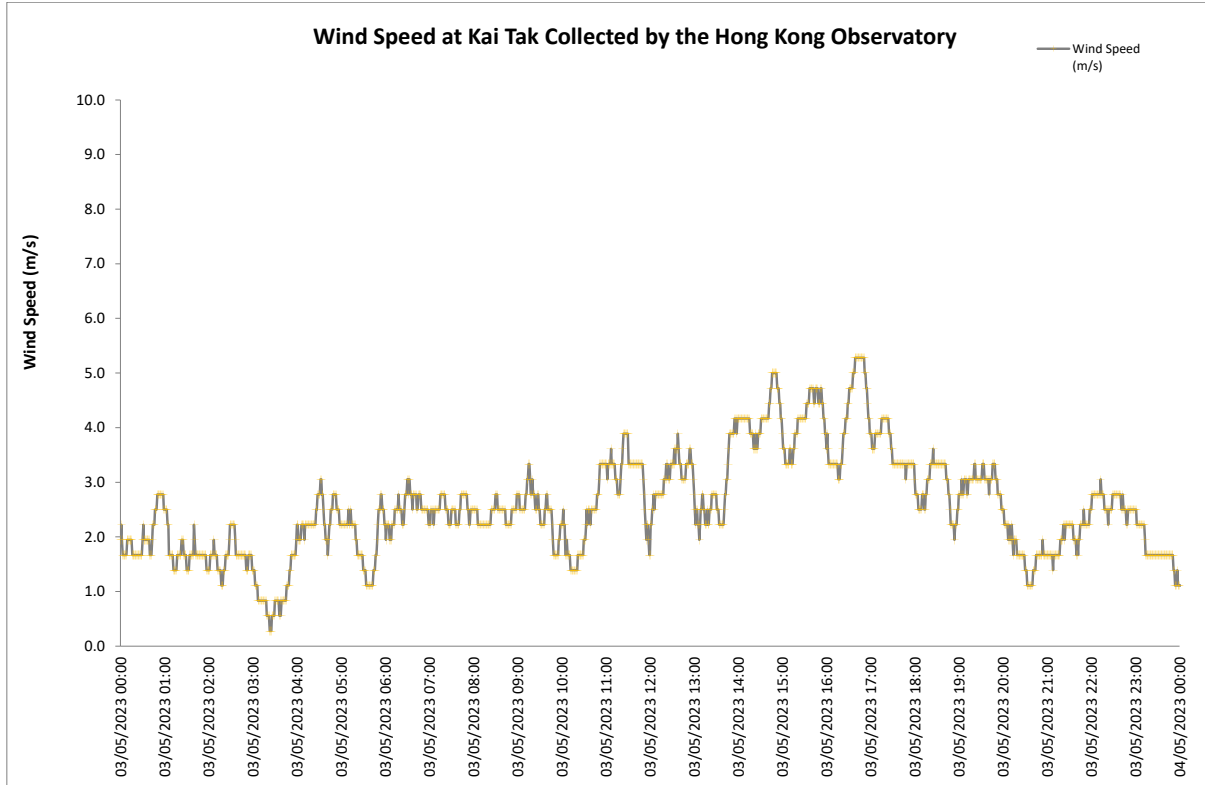



9 May 2023

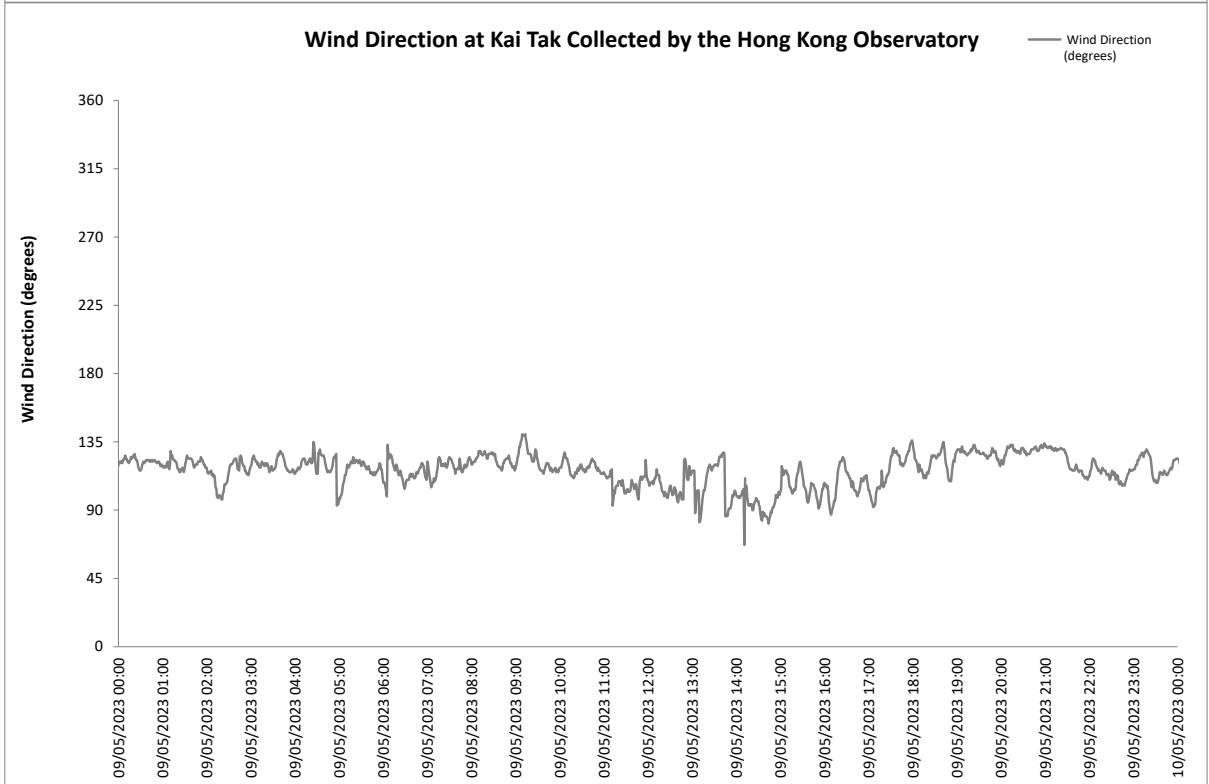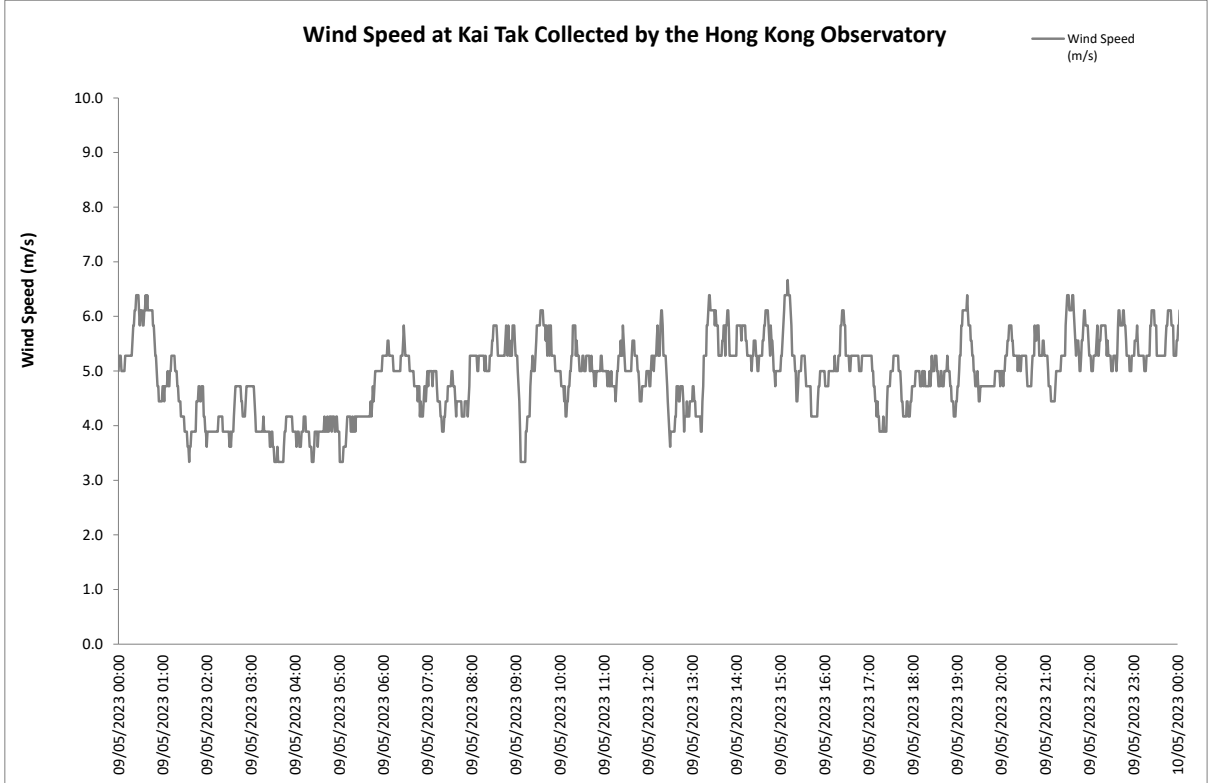



15 May 2023

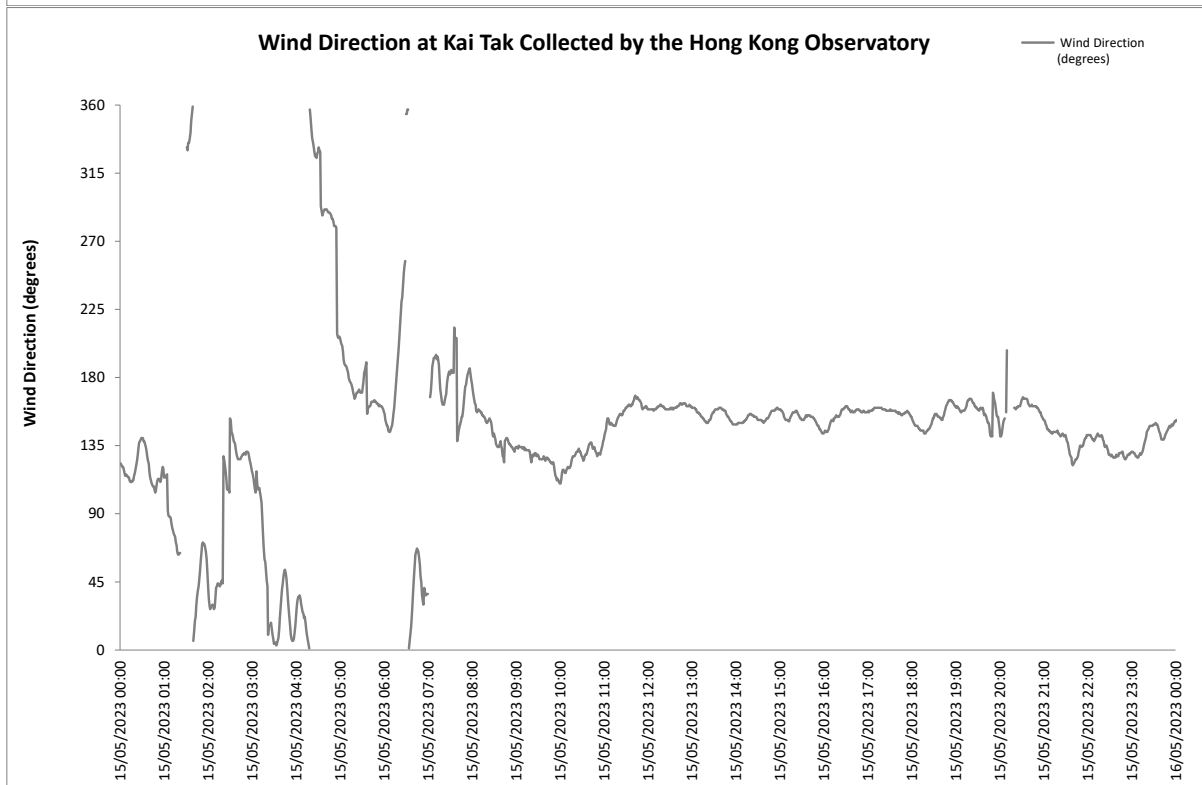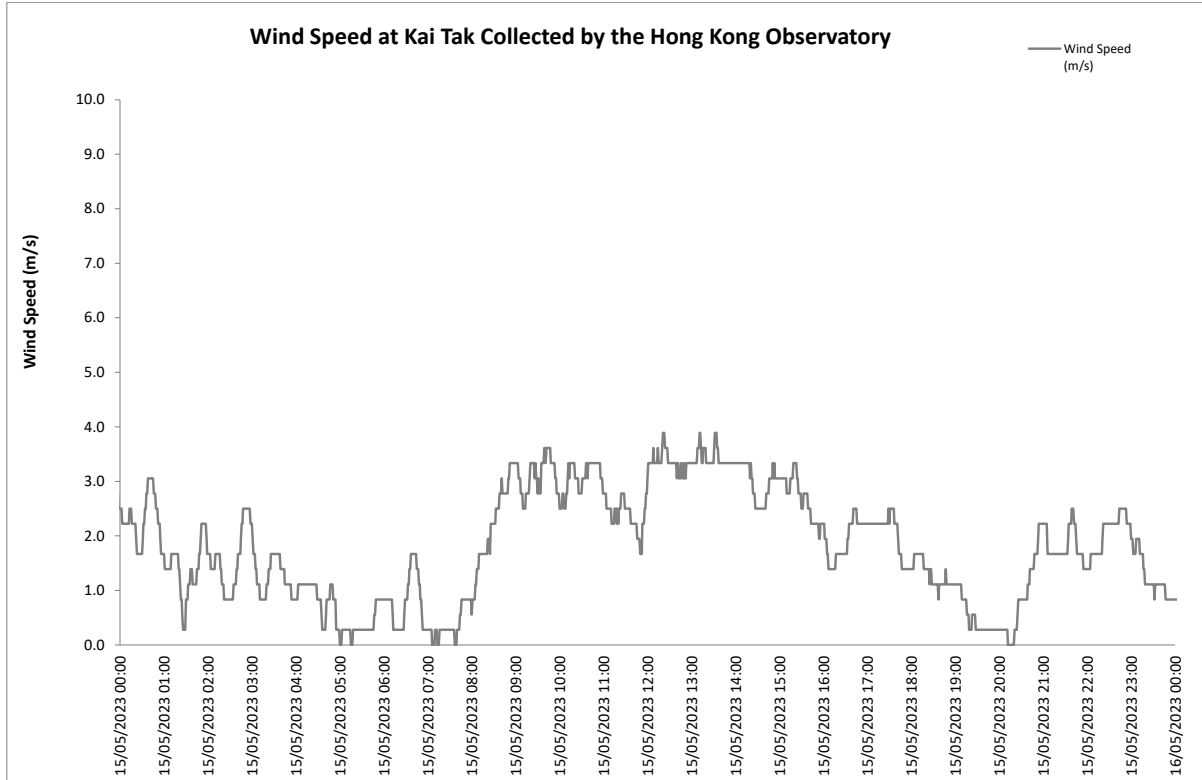



19 May 2023

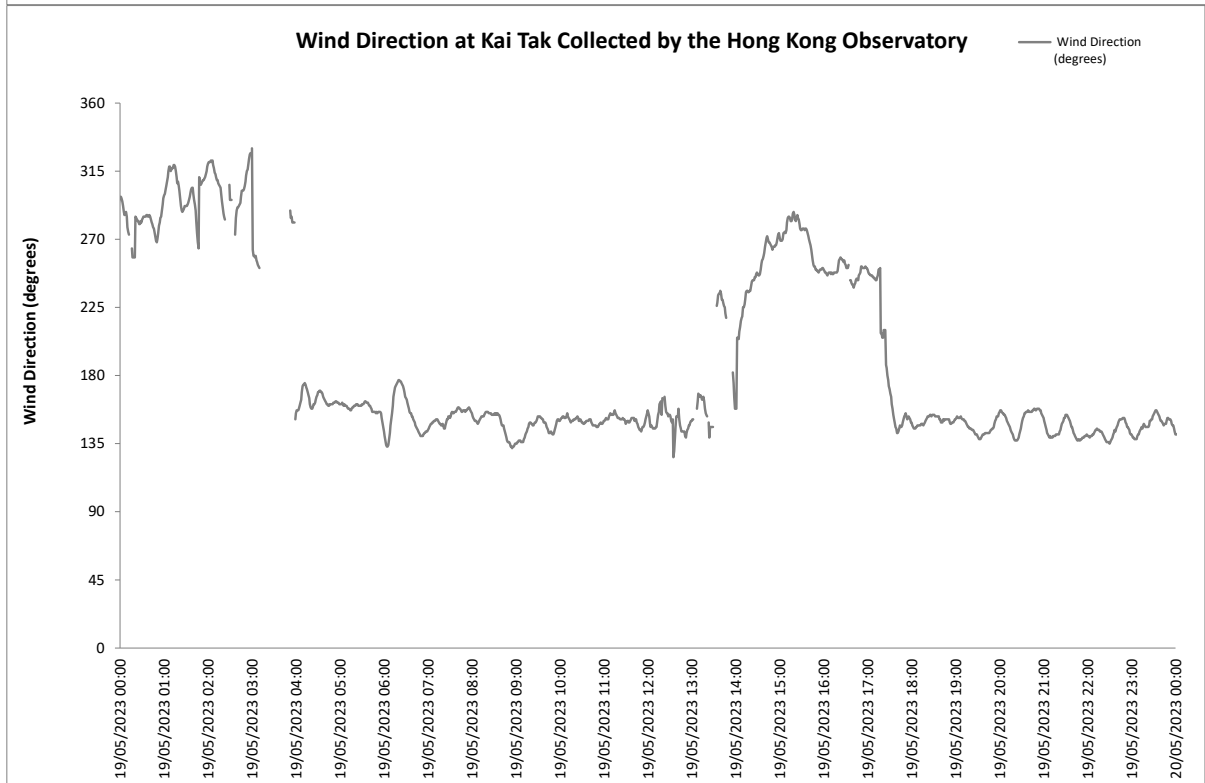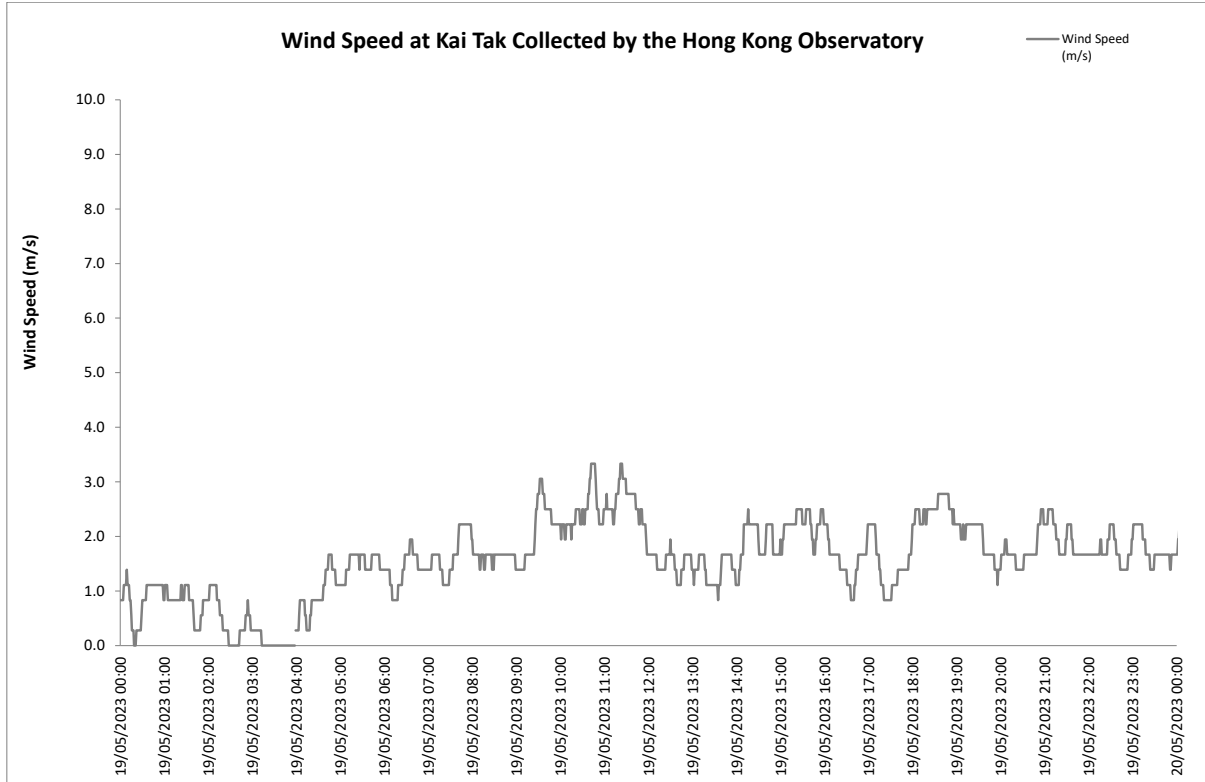



24 May 2023

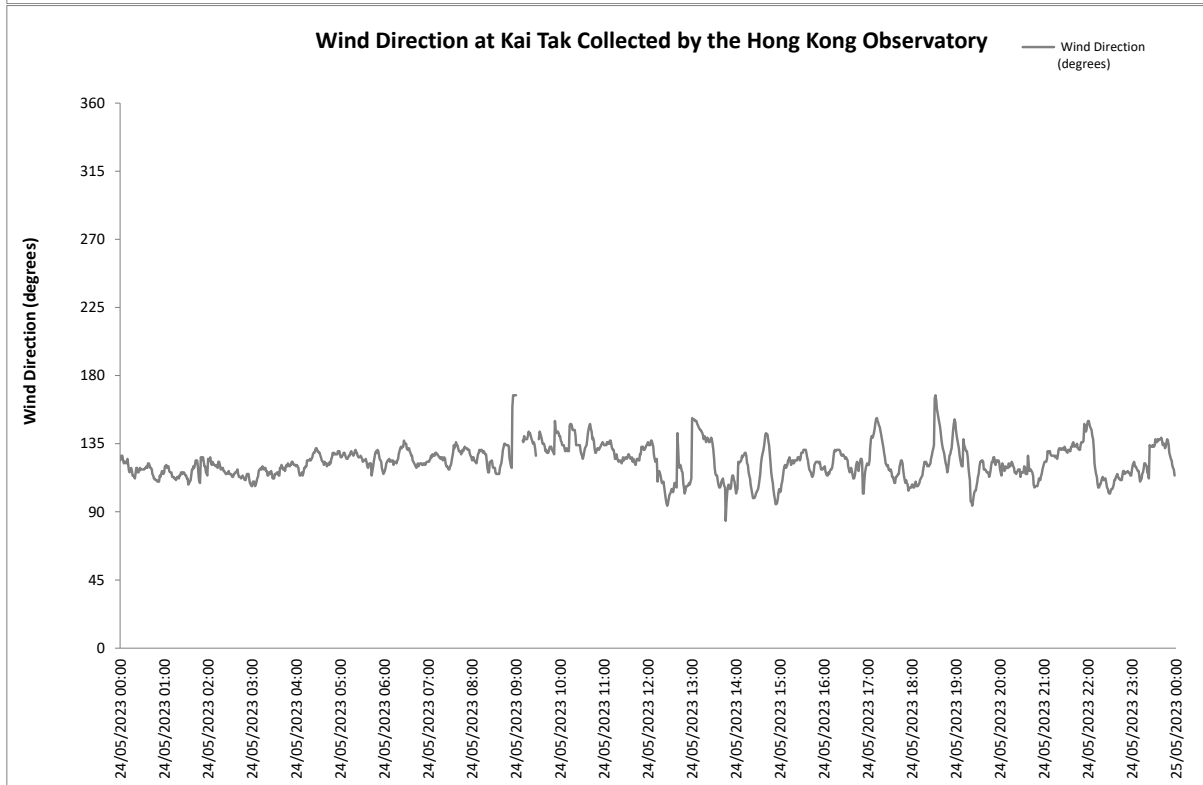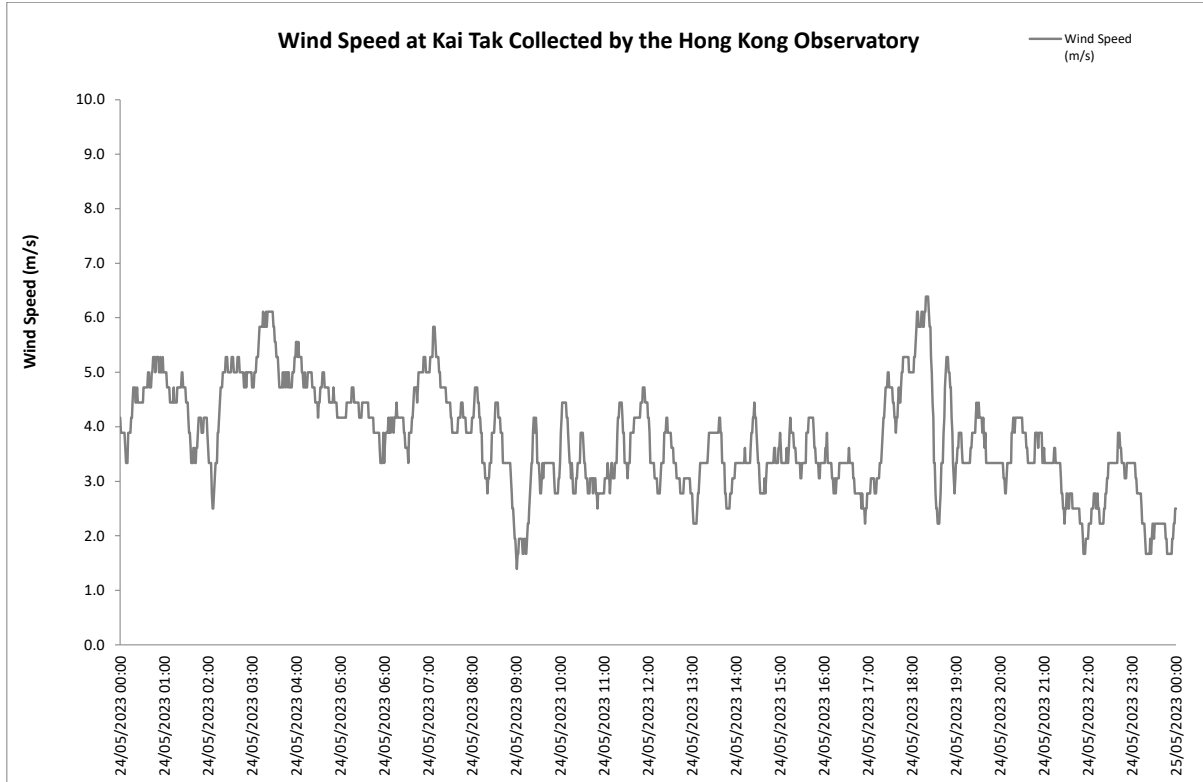


30 May 2023

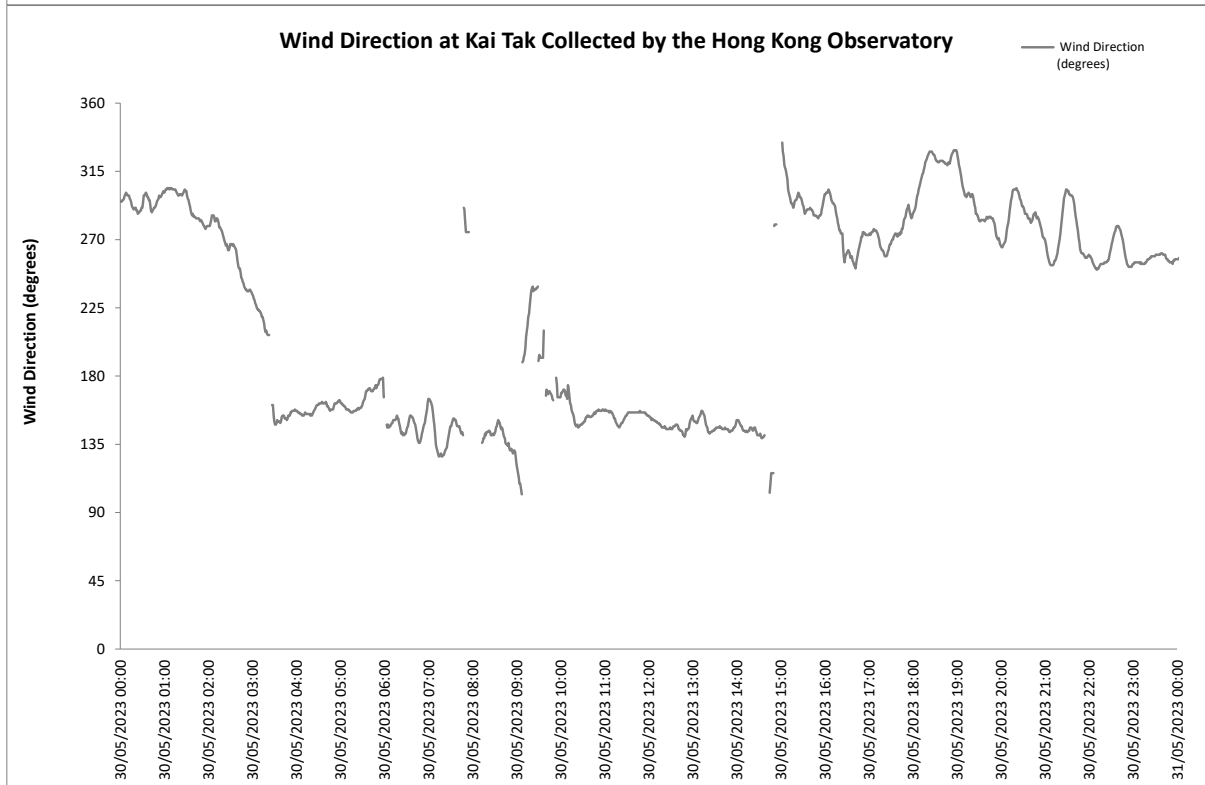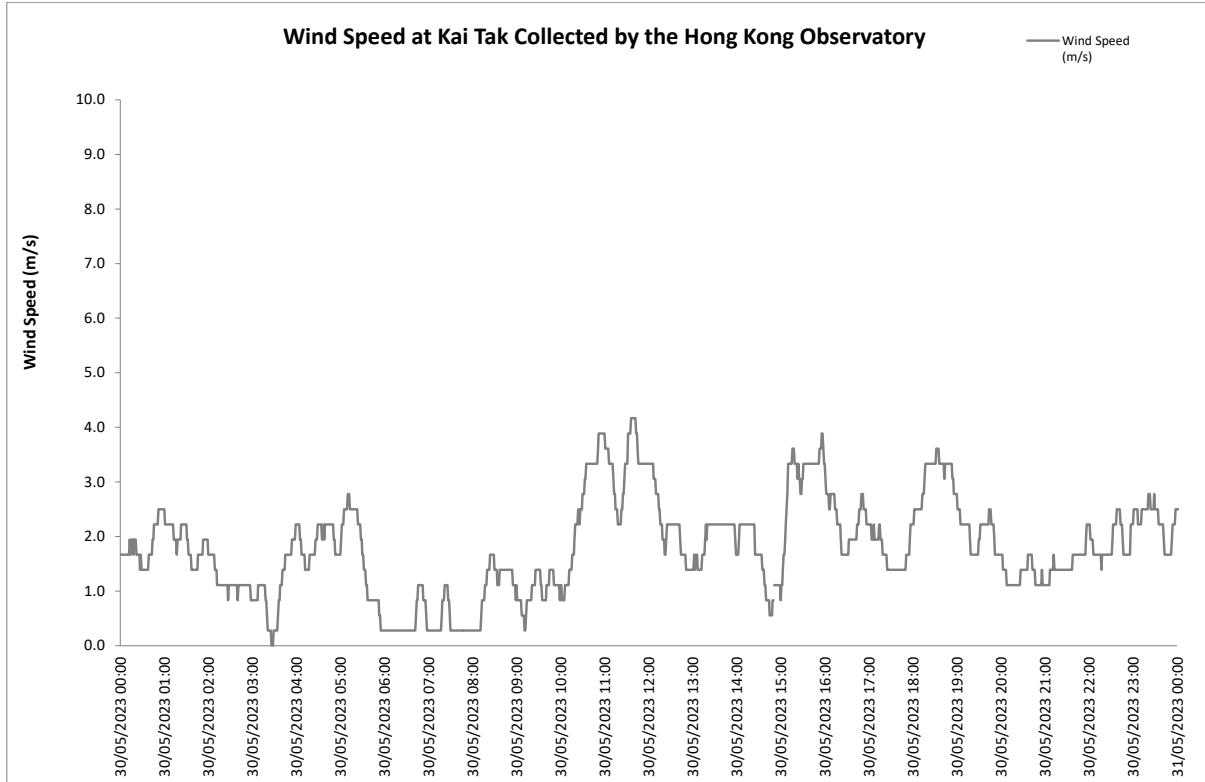



5 June 2023

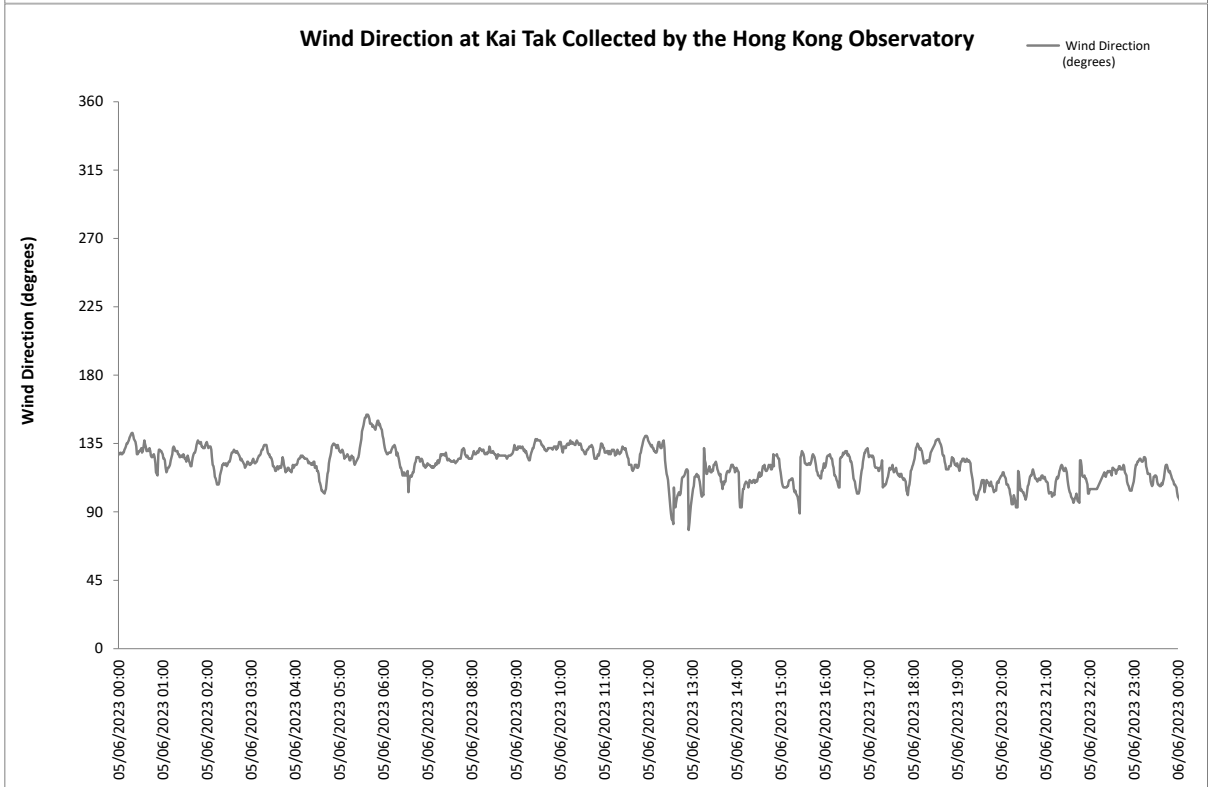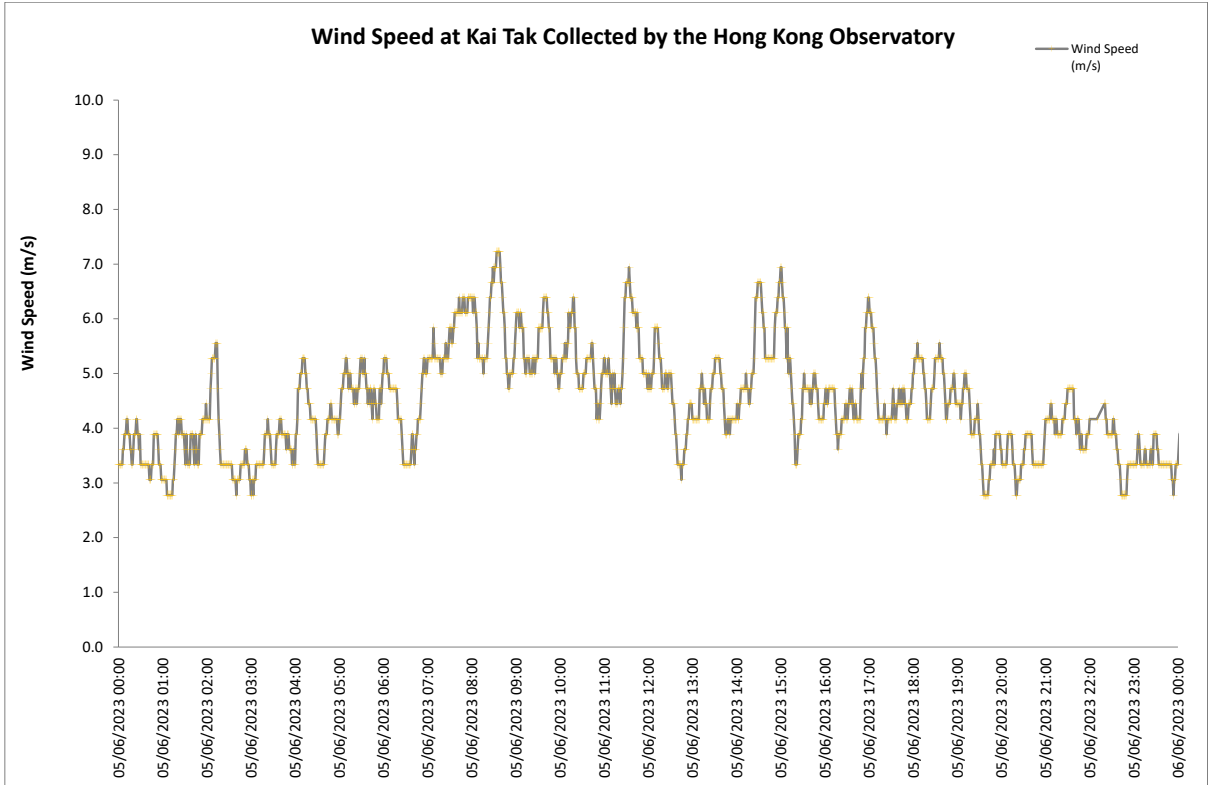



9 June 2023

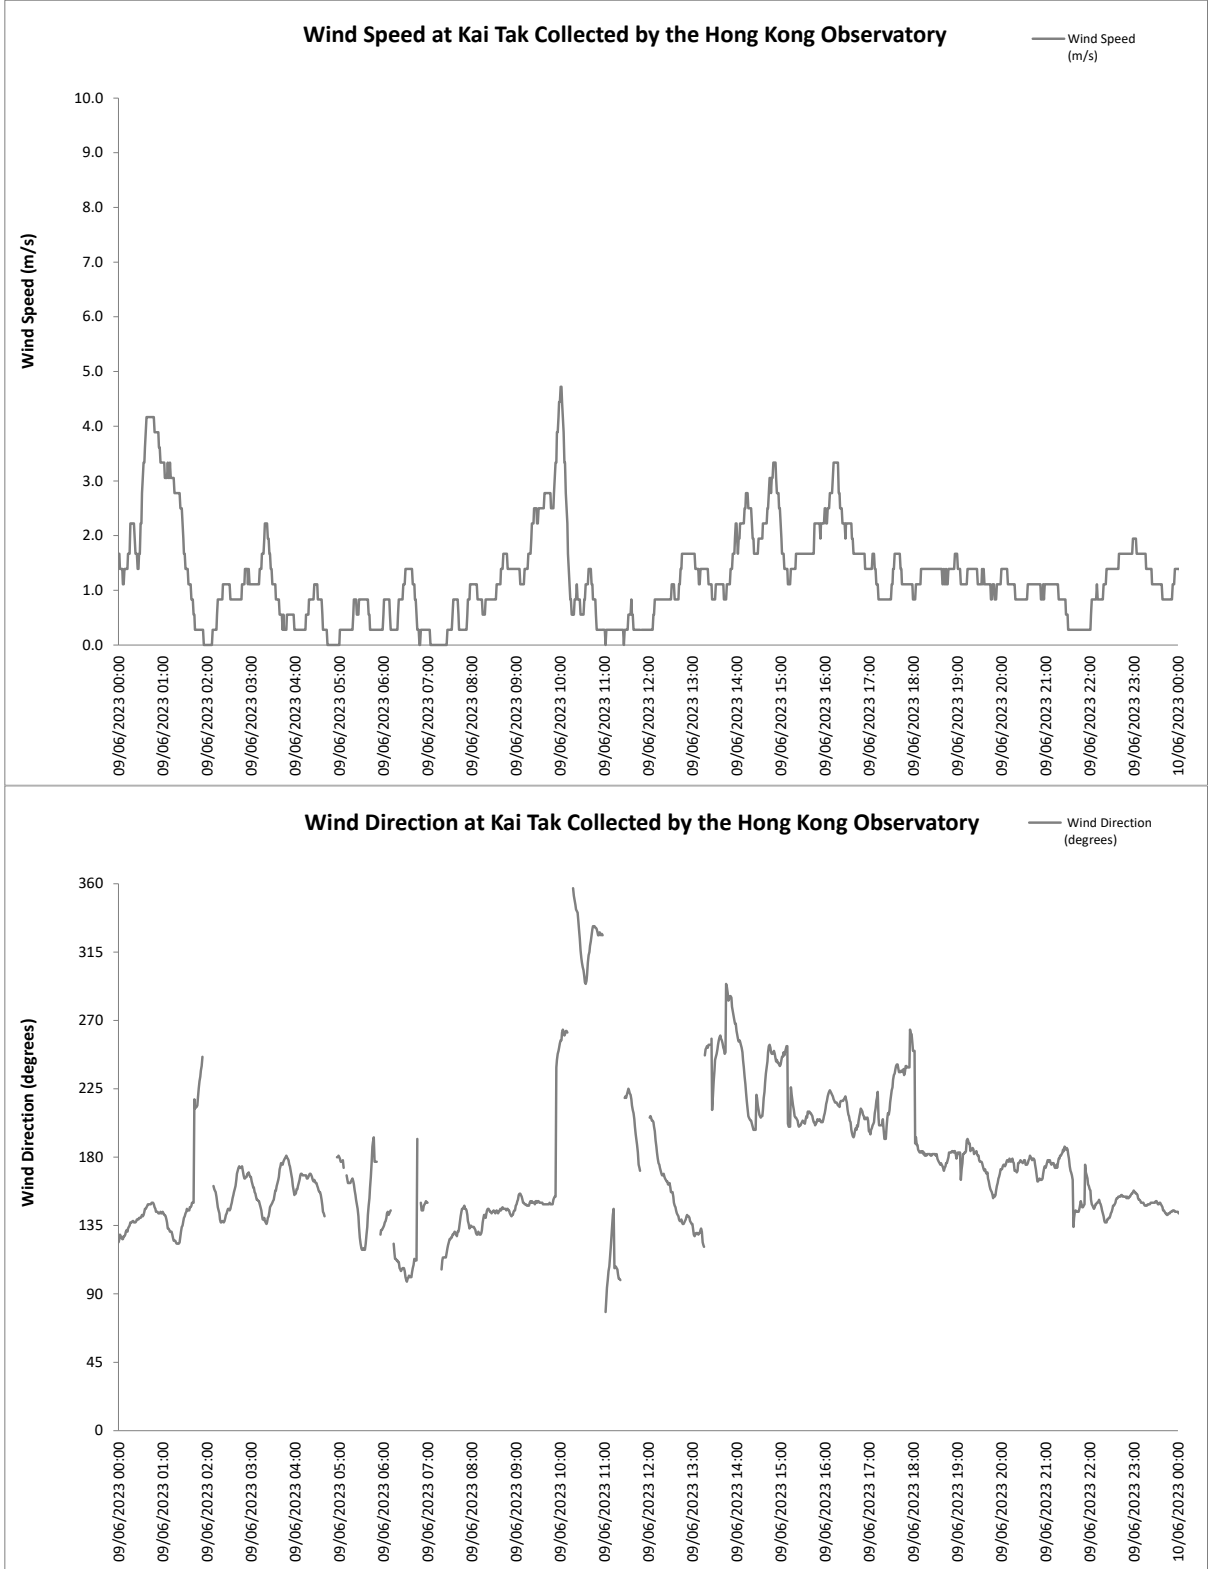



15 June 2023

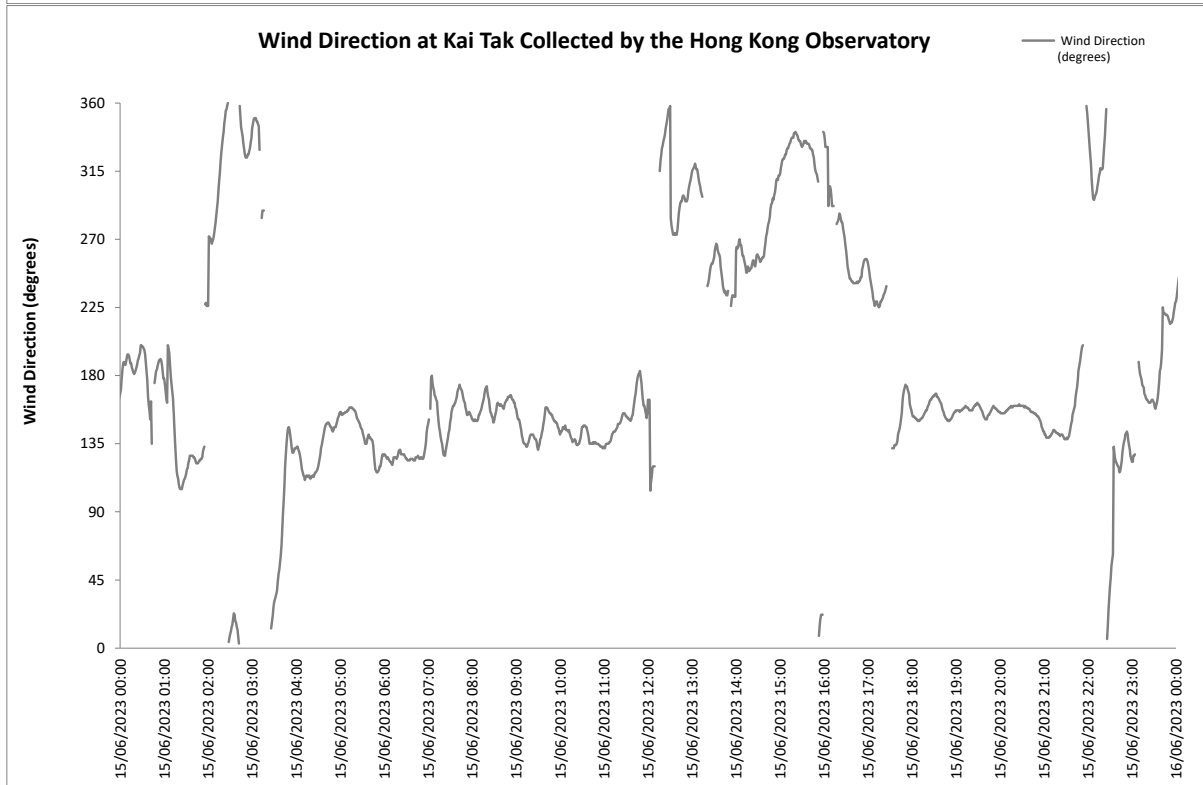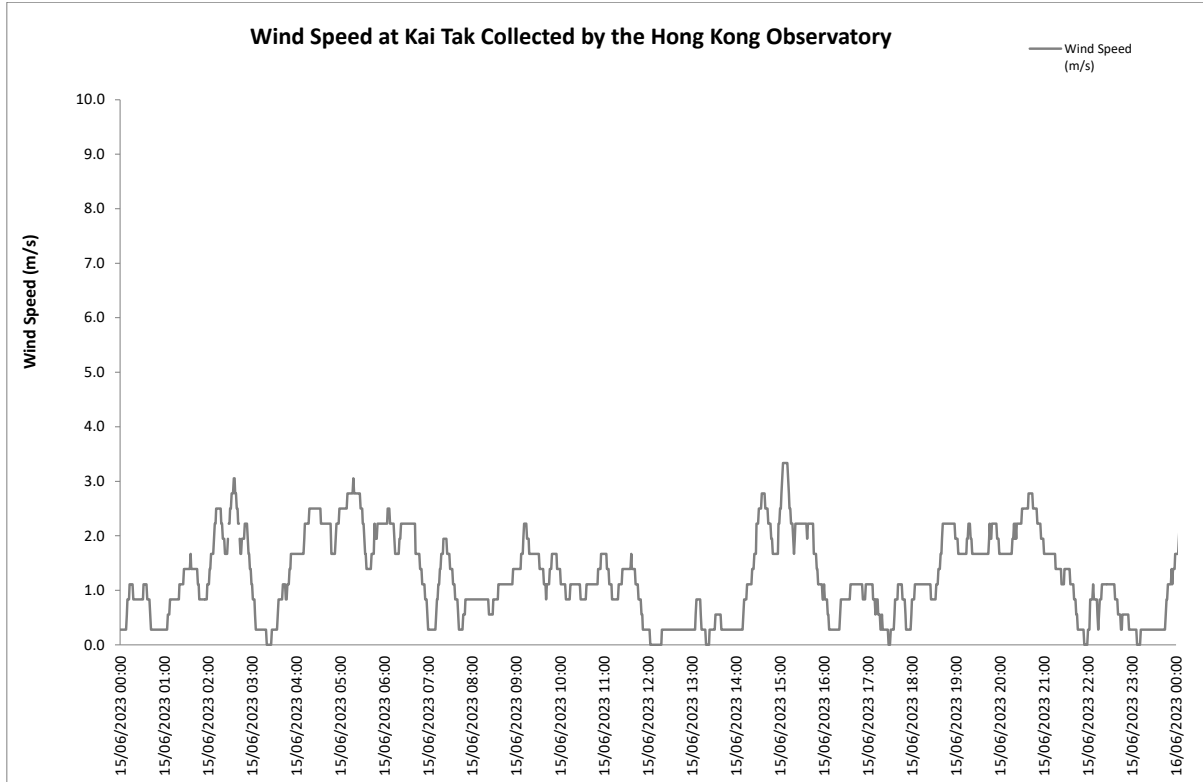

21 June 2023

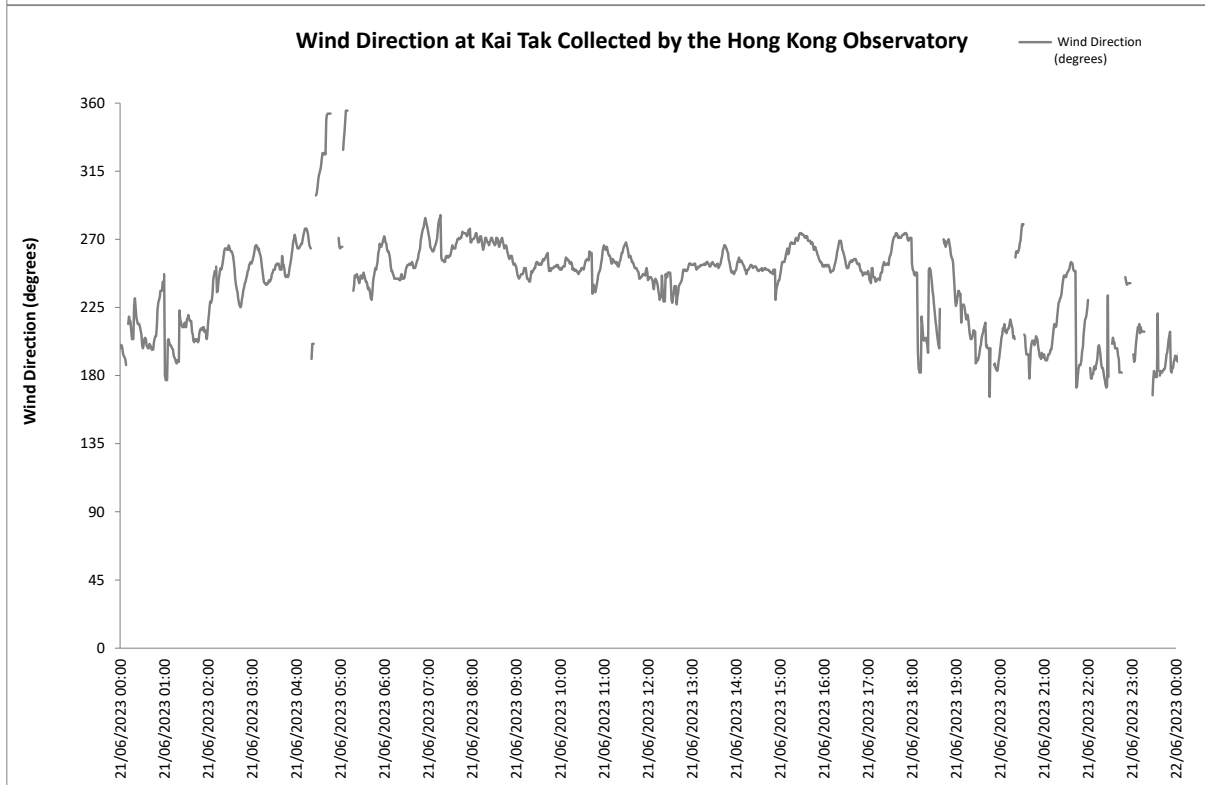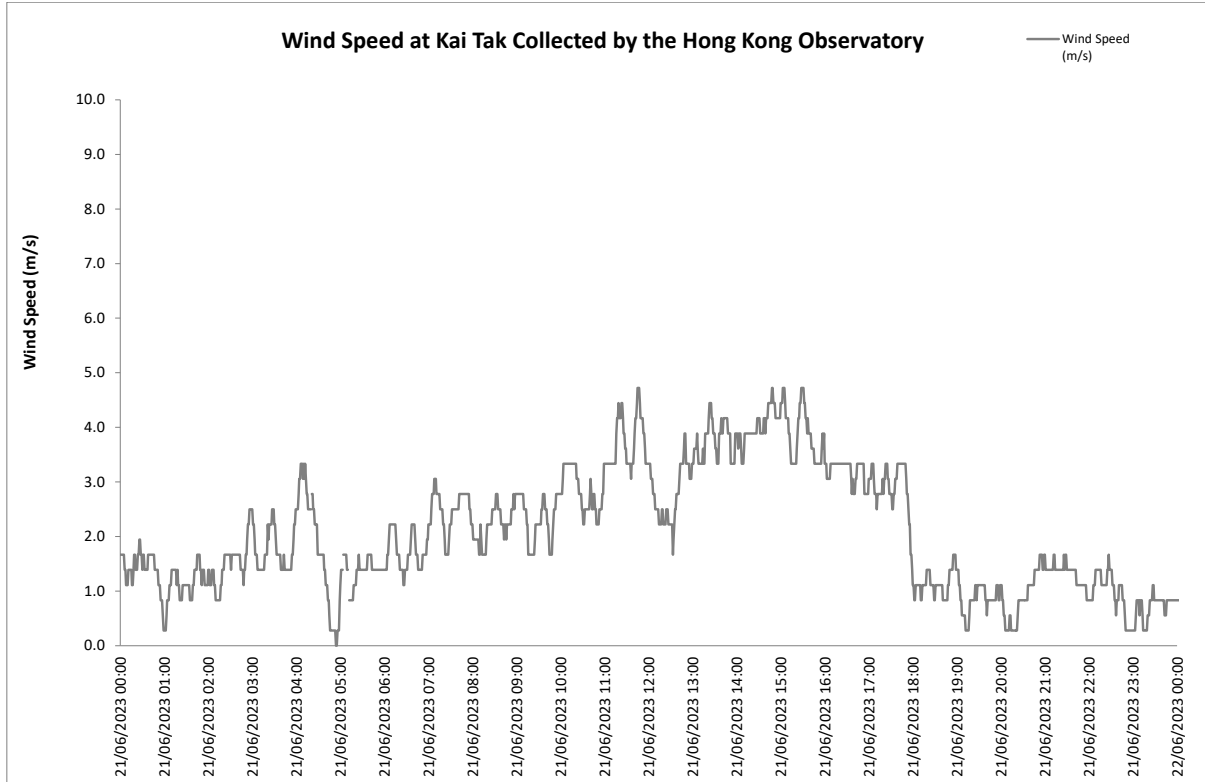

27 June 2023

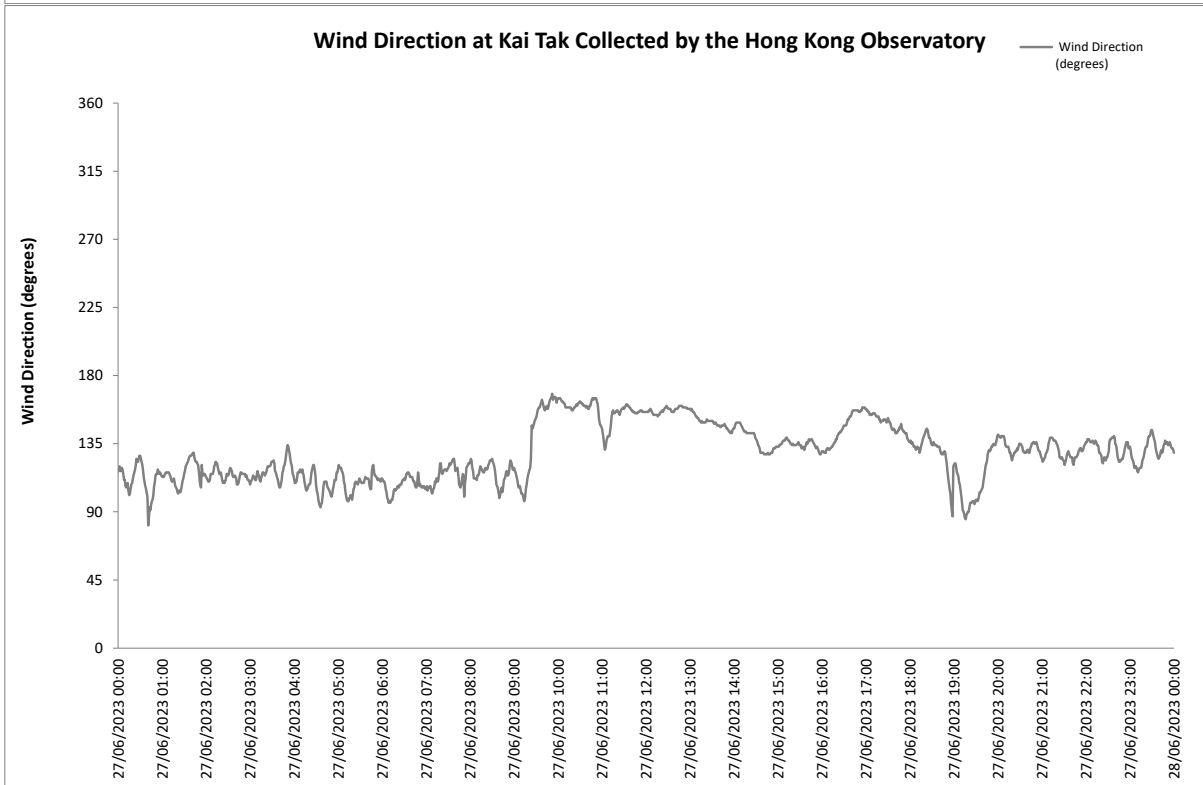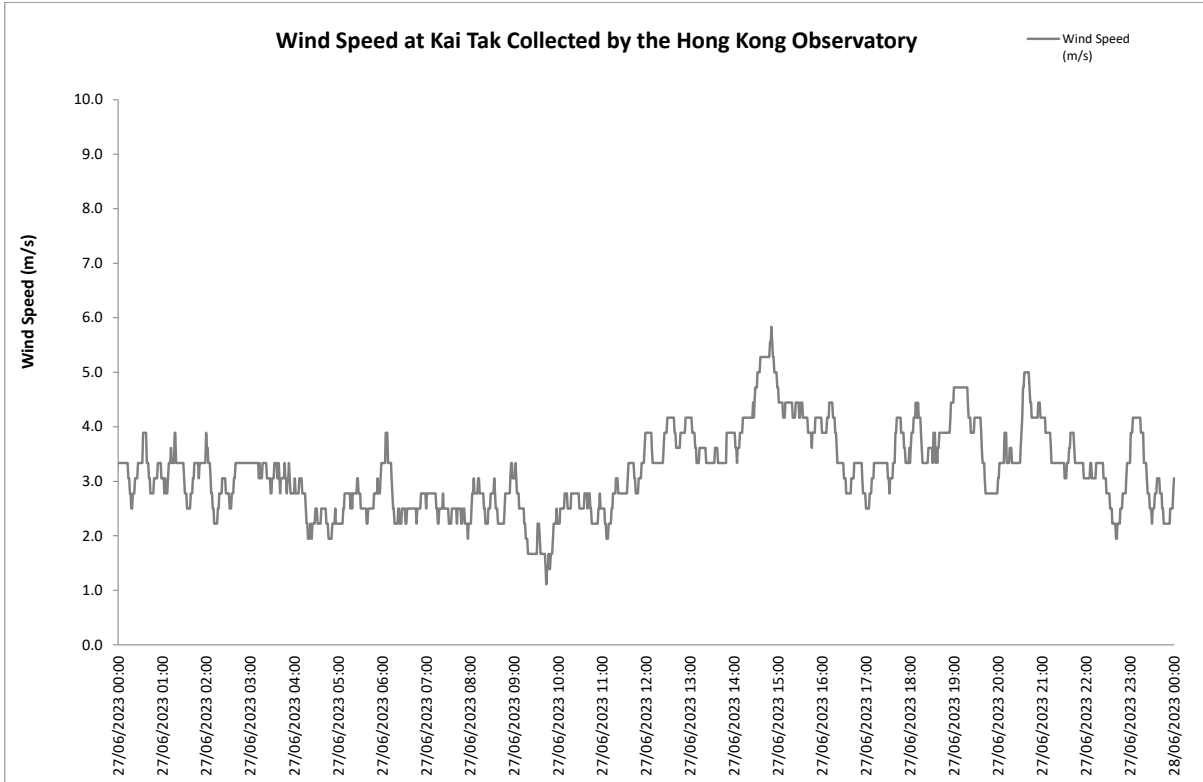

Appendix G. Waste Flow Table

Project: Kai Tak Sport Park
 Contract No.: HAB/ KTSP/ 01
 Contract Title: Design, Construction and Operation of the Kai Tak Sports Park at Kai Tak, Kowloon City District, Hong Kong
 Year of Record: 2019-2023



Monthly Waste Flow Table

Month	Total Quantity Generated	Total Quantity Generated (Excluded Excavated Material)	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Materials Generated Monthly						Remarks
			Excavated Materials			Non-excavated Materials					Metals (steel bar / metal strip) ⁽¹⁾	Metals (aluminum can) ⁽¹⁾	Paper / cardboard packaging ⁽¹⁾	Plastics ^{(1) & (4)}	Chemical waste (wasted lubricant oil/ oil container)	Other, e.g. general refuse	
			Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities							
(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)		
a1	a2	b	b	b	c	d	e	f	g	h	i	j	k	l	m		
2019	43517.88	8326.30	35191.58	0.00	0.00	0.00	0.00	0.00	0.00	166.07	0.00	2.05	7.92	2.00	8148.27		
2020	811029.24	6341.58	49326.08	0.00	755361.58	0.00	0.00	0.00	0.00	3170.12	0.47	10.10	20.71	2.20	3137.98		
Jan-21	78129.57	1315.84	4253.06	0.00	72560.67	0.00	0.00	0.00	0.00	393.38	0.05	2.68	1.96	0.00	917.77		
Feb-21	70013.03	912.17	10767.60	0.00	58333.26	0.00	0.00	0.00	0.00	386.46	0.07	1.24	0.64	0.00	523.76		
Mar-21	51743.64	1314.81	18740.08	0.00	31688.75	0.00	0.00	0.00	0.00	320.13	0.12	2.08	2.45	0.00	990.03		
Apr-21	16431.34	1411.19	0.00	0.00	15020.15	0.00	0.00	0.00	0.00	467.54	0.02	1.84	1.70	0.00	940.09		
May-21	39675.06	1610.42	0.00	0.00	38064.64	0.00	0.00	0.00	0.00	442.35	0.00	1.31	2.81	0.00	1163.95		
Jun-21	56589.31	1812.39	0.00	0.00	54776.92	0.00	0.00	0.00	0.00	353.07	0.02	1.10	1.37	0.00	1456.83		
Jul-21	18264.19	2544.22	0.00	0.00	15719.97	0.00	0.00	0.00	0.00	383.64	0.00	1.55	3.36	0.00	2155.67		
Aug-21	7959.53	2028.39	4150.75	0.00	1780.39	0.00	0.00	0.00	0.00	326.91	0.00	1.28	1.40	0.00	1698.80		
Sep-21	32389.58	2259.89	30129.69	0.00	0.00	0.00	0.00	0.00	0.00	269.75	0.00	1.99	2.68	0.00	1985.47		
Oct-21	34559.10	2034.74	17144.35	0.00	15380.01	0.00	0.00	0.00	0.00	289.21	0.00	1.04	2.83	0.00	1741.66		
Nov-21	34821.07	2353.58	6551.45	0.00	25916.04	0.00	0.00	0.00	0.00	164.09	0.00	1.27	3.80	0.60	2183.82		
Dec-21	10648.02	2282.17	8365.85	0.00	0.00	0.00	0.00	0.00	0.00	125.27	0.00	1.54	0.69	0.00	2154.67		
Jan-22	6238.85	2367.85	3871.00	0.00	0.00	0.00	0.00	0.00	0.00	130.89	0.00	1.43	1.76	0.00	2233.77		
Feb-22	6654.84	1294.33	5360.51	0.00	0.00	0.00	0.00	0.00	0.00	158.11	0.00	0.51	0.00	0.00	1135.71		
Mar-22	27279.95	1820.78	25459.17	0.00	0.00	0.00	0.00	0.00	0.00	162.33	0.00	0.81	0.85	0.00	1656.79		
Apr-22	15402.21	1792.21	13610.00	0.00	0.00	0.00	0.00	0.00	0.00	36.78	0.00	0.62	3.11	0.00	1751.70		
May-22	8425.54	2151.70	6273.84	0.00	0.00	0.00	0.00	0.00	0.00	83.12	0.00	0.61	1.47	0.00	2066.50		
Jun-22	8171.01	2700.44	5470.57	0.00	0.00	0.00	0.00	0.00	0.00	192.21	0.00	1.66	1.91	0.00	2504.66		
Jul-22	5804.34	2575.55	3228.79	0.00	0.00	0.00	0.00	0.00	0.00	238.36	0.00	1.56	4.87	0.00	2330.75		
Aug-22	11860.09	2557.97	9302.12	0.00	0.00	0.00	0.00	0.00	0.00	138.66	0.00	0.92	4.03	0.00	2414.36		
Sep-22	14721.29	2391.62	12329.67	0.00	0.00	0.00	0.00	0.00	0.00	155.67	0.00	0.52	5.72	0.00	2229.71		
Oct-22	12307.08	2428.20	9878.88	0.00	0.00	0.00	0.00	0.00	0.00	15.57	0.00	1.00	0.73	0.00	2411.40		
Nov-22	16034.69	2332.38	13702.31	0.00	0.00	0.00	0.00	0.00	0.00	83.73	0.00	0.57	1.24	0.00	2246.34		
Dec-22	21702.52	1944.12	19758.40	0.00	0.00	0.00	0.00	0.00	0.00	14.41	0.00	0.81	1.96	0.00	1926.94		
Jan-23	14065.32	1261.42	12803.90	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.66	1.54	0.00	1259.22		
Feb-23	17813.51	1729.85	16083.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.43	1.83	0.00	1726.59		
Mar-23	14767.87	2148.99	12618.88	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.96	3.68	0.00	2144.35		
Apr-23	13579.71	1411.83	12167.88	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.80	3.06	0.00	1407.97		
May-23	9704.79	1744.90	7959.89	0.00	0.00	0.00	0.00	0.00	0.00	7.05	0.00	0.32	4.02	0.00	1733.51		
Jun-23	8426.09	1558.40	6867.69	0.00	0.00	0.00	0.00	0.00	0.00	10.74	0.00	1.17	2.17	0.00	1544.32		
Total	1538730.25	72760.22	381367.65	0.00	1084602.38	0.00	0.00	0.00	0.00	8685.62	0.75	47.42	98.27	4.80	63923.36		

Total C&D waste generated	1538730.25	tonne	a1=b+c+d+e+f+g+h+i+j+k+l+m
Total C&D waste generated (excluding excavated materials)	72760.22	tonne	a2=c+d+e+f+g+h+i+j+k+l+m
Total recycled C&D waste	8832.07	tonne	a3=c+d+e+h+i+j+k
% of recycled C&D waste for BEAM Plus MA10 or MA11	12.14	%	a4=a3/a2 x 100%

- Notes:
- (1) Metal, paper & plastic were collected by recycler.
 - (2) The performance target of waste recycling are specified in the Contract.
 - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
 - (5) Broken concrete for recycling into aggregates.
 - (6) Excavated materials/waste will **NOT** be considered as part of construction waste. It should be excluded in the calculation.
 - (7) Disposal of inert waste to public fill or sorting facilities will **NOT** be considered as recycled waste.
 - (8) Disposal record for April 2023 and May 2023 have been updated according to the latest information from contractor in June 2023.
 - (9) Recycling record for metals, papers and plastics have been updated according to the latest information from contractor in June 2023.

Project: Proposed Composite Development at NKIL 6607, Shing Kai Road, Kai Tak, Kowloon

Company: Hip Hing Construction Co., Ltd.

Monthly Summary Waste Flow Table

Month	Total Quantities Generated	Total Quantities Generated (excluded excavated material)	Accumulated Quantities of Inert C&D Materials Generated Monthly					Accumulated Quantities of Non-inert C&D Wastes Generated Monthly						
			(a)	(b)	(c)	(d)	(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)
			Broken Concrete Recycled	Broken Concrete Diverted to Public Fill	Excavated Materials Reused in this Project	Excavated Materials Reused in other Projects	Excavated Materials Disposed as Public Fill	Mixed Wastes Diverted to Sorting Facility	Metals Recycled	Paper/ Cardboard Packaging Recycled	Timber/Wood Pallet Recycled	Plastics Recycled	Chemical Waste Collected	Others, e.g. General Refuse Disposed at Landfill
			(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)
Aug-21	0	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Sep-21	1550.68	0.00	0	0	0	1550.68	0.00	0.00	0.00	0.00	0	0	0	0.00
Oct-21	3691.90	28.13	0	0	0	3663.77	0.00	0.00	13.17	0.00	0	0	0	14.96
Nov-21	5447.65	68.57	0	0	0	5309.20	69.88	6.05	32.40	0.00	0	0	0	30.12
Dec-21	400.90	180.45	0	0	0	63.20	157.25	0.00	138.58	0.00	0	0	0	41.87
Jan-22	1454.58	288.36	0	0	0	493.40	672.82	27.52	245.57	0.00	0	0	0	15.27
Feb-22	241.23	207.42	0	0	0	0.00	33.81	4.65	177.65	0.05	0	0	0	25.07
Mar-22	1717.06	373.58	0	0	0	0.00	1343.48	89.56	265.79	0.00	0	0	0	18.23
Apr-22	1657.01	788.84	0	0	0	0.00	868.17	87.83	684.33	0.00	0	0	0	16.68
May-22	1260.80	124.46	0	0	0	0.00	1136.34	102.49	21.97	0.00	0	0	0	0.00
Jun-22	464.11	77.27	0	0	0	0.00	386.84	55.75	21.43	0.09	0	0	0	0.00
Jul-22	813.76	98.52	0	0	0	0.00	715.24	58.30	32.29	0.00	0	0	0	7.93
Aug-22	442.84	55.11	0	0	0	0.00	387.73	54.95	0.00	0.16	0	0	0	0.00
Sep-22	786.99	91.80	0	0	0	0.00	695.19	91.80	0.00	0.00	0	0	0	0.00
Oct-22	1428.67	157.88	0	0	0	0.00	1270.79	154.05	0.00	0.00	0	0	0	3.83
Nov-22	2134.86	174.01	0	0	0	0.00	1960.85	147.07	0.00	0.63	0	0	0	26.31
Dec-22	864.13	212.59	0	0	0	0.00	651.54	198.44	0.00	0.00	0	0	0	14.15
Jan-23	885.60	135.88	0	0	0	0.00	749.72	133.59	0.00	0.00	0	0	0	2.29
Feb-23	1286.59	225.50	0	0	0	0.00	1061.09	181.53	24.35	0.52	0	0	0	19.10
Mar-23	691.22	253.47	0	0	0	0.00	437.75	149.17	71.86	0.16	0	0	0	32.28
Apr-23	3744.20	56.11	0	0	0	0.00	3688.09	30.39	0.00	0.28	0	0	0	25.44
May-23	2229.07	11.84	0	0	0	0.00	2217.23	5.92	0.00	0.00	0	0	0	5.92
Jun-23	97.56	84.02	0	0	0	0.00	13.54	82.67	0.00	0.00	0	0	0	1.35
Total	33291.41	3693.81	0	0	0	11080.25	18517.35	1661.73	1729.39	0.93	0.00	0.00	0.00	300.80

Total C&D Waste generated 33291.41 Tons
 Total C&D waste generated (Excluded excavated materials) 3693.81 Tons
 Total C&D waste recycled 1730.32 Tons

$$\text{Waste Recycling Rate} = \frac{(a) + (g) + (h) + (i) + (j)}{(a) + (b) + (f) + (g) + (h) + (i) + (j) + (l)} \times 100\% = 46.84\%$$

Note:

For BEAM Plus certification scheme, excavated materials are excluded from the calculation of the waste reduction rate Record with Underlined indicated updated content

Appendix H. Environmental Licences and Permits

Table H.1: Summary of Environmental Licences and Permits Status (KTSP)

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	441733	25 Jan 2019	29 Jan 2019	N/A	N/A
3	Construction Waste Disposal Account (Main)	7033182	12 Feb 2019	12 Feb 2019	N/A	N/A
4	Construction Waste Disposal Account (Vessel)	7033555	11 Jul 2022	10 Aug 2022	10 Nov 2022	Issued
5	Registration as a Chemical Waste Producer	WPN5213-286-H3906-02	29 Jan 2019	12 Feb 2019	N/A	N/A
6	Discharge Licence under WPCO	WT00034082-2019	15 Feb 2019	26 Jun 2019	30 Jun 2024	Issued
7	Construction Noise Permit (Construction Works, Northern Site)	GW-RE1068-22	22 Sep 2022	30 Oct 2022	29 Apr 2023	Superseded by GW-RE0400-23 on 30 Apr 2023.
8	Construction Noise Permit (Construction Works, Southern Site)	GW-RE1157-22	11 Oct 2022	25 Nov 2022	20 May 2023	Superseded by GW-RE0425-23 on 24 May 2023
9	Construction Noise Permit (Construction Works, Barging Point)	GW-RE1227-22	3 Nov 2022	21 Nov 2022	20 May 2023	Superseded by GW-RE0522-23 on 21 May 2023
10	Construction Noise Permit (Special Truss Delivery Port)	GW-RE1347-22	28 Nov 2022	6 Jan 2023	5 Apr 2023	Superseded by GW-RE0236-23 on 6 Apr 2023.

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
11	Construction Noise Permit (Special Shing Kai Road)	GW-RE1458-22	21 Dec 2022	1 Feb 2023	29 Apr 2023	Issued
12	Construction Noise Permit (Special Truss Delivery Port)	GW-RE0236-23	27 Feb 2023	6 Apr 2023	5 Jul 2023	Issued
13	Construction Noise Permit (Construction Works, Northern Site)	GW-RE0400-23	23 Mar 2023	30 Apr 2023	29 Jul 2023	Issued
14	Construction Noise Permit (Construction Works, Southern Site)	GW-RE0425-23	11 Apr 2023	24 May 2023	23 Aug 2023	Issued
15	Construction Noise Permit (Construction Works, Barging Point)	GW-RE0522-23	27 Apr 2023	21 May 2023	20 Nov 2023	Issued

Table H.2: Summary of Environmental Licences and Permits Status (H/O Development)

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	458255	17 Jul 2020	17 Jul 2020	N/A	N/A
		470045	29 Jul 2021	29 Jul 2021	N/A	N/A
3	Construction Waste Disposal Account (Main)	7041267	29 Jul 2021	11 Aug 2021	N/A	Issued
4	Registration as a Chemical Waste Producer	WPN5211-286-H1103-23	29 Jul 2021	24 Aug 2021	N/A	Issued
5	Discharge Licence under WPCO	WT00039490-2021	6 Aug 2021	9 Nov 2021	30 Nov 2026	Issued
6	Construction Noise Permit	GW-RE1321-22	22 Nov 2022	2 Jan 2023	1 Jun 2023	Superseded by GW-RE0494-23 on 2 Jun 2023
7	Construction Noise Permit	GW-RE0494-23	14 Apr 2023	2 Jun 2023	1 Nov 2023	Issued

Appendix I. Environmental Mitigation Measures Implementation Status

Air Quality – Recommended Mitigation Measures

Air Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Good housekeeping to minimize dust generation, e.g. by properly handling and storing dusty materials	P	✓
• Store cement in shelter with 3 sides and the top covered by impervious materials if the stack exceeds 20 bags	✓	✓
• Cement delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed	N/A	N/A
• Loading, unloading, transfer, handling or storage of bulk cement should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system	✓	✓
• Dusty materials (e.g. debris) should be wetted by misting / water-spraying before any loading, unloading, transfer or transport operation	✓	✓
• Any skip hoist for material transport should be fully enclosed by impervious sheeting	✓	✓
• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously	✓	P
• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities to maintain the entire surface wet	✓	✓
• Excavation area should be minimized as far as possible	✓	✓
• Stockpile of dusty materials should not be extended beyond the pedestrian barriers, fencing or traffic cones	✓	✓
• Excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet, and then removed, backfilled or reinstated where practicable within 24 hours of the excavation or unloading	✓	P
• Dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads	✓	✓
• Properly fitted side and tail boards are necessary for any vehicle with open load area	✓	✓
• While transporting materials that potentially create dust (e.g. debris), materials should not be loaded higher than side and tail boards, and should be fully covered by tarpaulin or similar materials which extend at least 300 mm over the edges of the side and tail boards to prevent leakage.	✓	✓
• Limit the maximum vehicle speed within the site to 10km/hr	✓	✓
• Haulage and delivery vehicles should be confined to designated roads	✓	✓
• Every main haul road should either be 1.) paved with concrete and kept clear of dusty materials, or 2.) sprayed or watered to maintain the entire road surface wet	✓	P
• All on-site unpaved roads should be compacted and kept free of loose materials as possible	✓	✓
• Provide vehicle washing (e.g. wheel washing bay & high pressure water jet where practicable) at every vehicle exit point for cleaning vehicle body and wheels	✓	✓
• The vehicle washing area and the road between washing area and site exit should be paved with concrete, bituminous or other hardcores	✓	✓
• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials.	P	P
• Dusty materials on every vehicle's body and wheels should be removed in washing area before leaving the site	✓	✓

• Regular maintenance of all plant equipment	✓	✓
• Throttle down or switch off unused machines or machine in intermittent use	✓	✓
• If the site is adjacent to area where accessible to the public (e.g. road and service lane etc.), hoarding of not less than 2.4 m high from ground level should be erected along the adjoining the entire length of that portion of the site boundary, except for a site entrance or exit. The hoarding should be well maintained throughout the construction period.	✓	✓
• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding	✓	N/A
• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies	✓	✓
• Carry out air quality monitoring throughout the construction period	✓	✓
• Carry out weekly site inspection to audit the implementation of mitigation measures	✓	✓
• Regular watering once per hour on exposed worksites and haul road with an equivalent intensity of not less than 1.3L/m ³ to achieve 91.7% dust removal efficiency.	✓	✓
• Provision of electrical vehicle (EV) charging facilities in at least one-third of the car parking spaces for private cars. Provision of EV charging enabling facilities in all car parking spaces provided for private cars.	✓	N/A
Non-Road Mobile Machinery (NRMMS)		
• All NRMMS operated on-site are approved or exempted (as the case may be) and affixed with the requisite approval/exemption labels under the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation or are in the process of application for such approval/exemption during the relevant grace period.	P	P

Noise – Recommended Mitigation Measures

Noise Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Adopt good site practice, such as throttle down or switch off equipment unused or intermittently used between works	✓	✓
• Regular maintenance of equipment to prevent noise emission due to impair	✓	✓
• Position mobile noisy equipment in locations away from NSRs and point the noise sources to directions away from NSRs	✓	✓
• Use silencer or muffler for equipment	✓	✓
• Make good use structures for noise screening	✓	✓
• Use Quality Powered Mechanical Equipment (QPME) and quiet equipment which produces lower noise level.	✓	✓
• Erect movable noise barrier of 3m height to shed large plant equipment (e.g. breaker, backhoe & mobile crane) or hand-held items (e.g. poker, wood saw, power rammer & compactor) near low-rise NSR. Where necessary, special design (e.g. with noise absorbing material or bend top) should be adopted. The barrier's length should be at least five times greater than its height, and the minimum surface density is 10 kg/m ² . Alternatively, acoustic shed, enclosure or silencer (for generator, air compressor and concrete pump) or acoustic mat (for piling) can be adopted.	✓	N/A
• Carry out regular site inspection to audit the implementation of mitigation measures	✓	✓
• Carry out noise monitoring throughout the construction period	✓	✓

Water Quality – Recommended Mitigation Measures

Water Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted.	✓	✓
• Install perimeter channels in the works areas to intercept runoff from boundary prior to the commencement of any earthwork	✓	✓
• To prevent storm runoff from washing across exposed soil surfaces, intercepting channels should be provided.	✓	✓
• Drainage channels are required to convey site runoff to sand/silt traps and oil interceptors. Provision of regular cleaning and maintenance to ensure the normal operation of these facilities throughout the construction period.	✓	✓
• Any practical options for the diversion and realignment of drainage should comply with both engineering and environmental requirements	✓	✓
• Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the existing WSD saltwater intake and EMSD cooling water intake.	✓	✓
• The following good site measures should be adopted for the use of the existing barging facilities being operated by the MTR SCL Project: - All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. - All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material. - Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site. - Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. - Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation. Whole construction site Contractor P WPCO, EIAO-TM Page	N/A	N/A
• The runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS.	P	✓
• Reuse and recycling of the treated effluent from construction site runoff.	✓	✓
• Weekly site audit should be carried out to check the implementation status of the recommended water quality impact mitigation measures throughout construction period.	✓	✓
• The construction programme should be properly planned to minimise soil excavation, if any, in rainy seasons.	✓	✓
• Any exposed soil surfaces should be properly protected to minimise dust emission.	✓	✓
• In areas where a large amount of exposed soils exist, earth bunds or sand bags should be provided.	✓	✓
• Exposed stockpiles should be covered with tarpaulin or impervious sheets at all times.	✓	✓
• The stockpiles of materials should be placed at locations away from any stream courses so as to avoid releasing materials into the water bodies.	✓	✓
• Final surfaces of earthworks should be compacted and protected by permanent work.	✓	✓
• Haul roads should be paved with concrete and the temporary access roads protected using crushed stone or gravel, wherever practicable.	✓	✓
• Wheel washing facilities should be provided at all site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.	P	P
• Good site practices should be adopted to keep the site dry and tidy, such as clean the rubbish and litter on the construction sites.	P	✓
• Adequate temporary site drainage and pumping should be provided, if necessary.	P	✓
• Provide sufficient temporary toilets in the works areas. The toilet facilities should be more than 30 m from any watercourse. A licensed waste collector should be deployed to clean the temporary toilets on a regular basis.	✓	✓
• Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project.	✓	✓

<ul style="list-style-type: none"> Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes. 	✓	✓
<ul style="list-style-type: none"> Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. 	✓	✓
<ul style="list-style-type: none"> Clean the construction sites on a regular basis. 	✓	✓
<ul style="list-style-type: none"> Oil interceptor in car parking area shall be designed and constructed according to Practice Note for Authorized Persons, Registered Structural Engineers and Registered Geotechnical Engineers, APP-46 (PNAP 124) 	✓	N/A
<ul style="list-style-type: none"> Provide two sequential storage tanks to contain surface water with residual fertilizers and pesticides and third holding tank for incidental rainstorm 	N/A	N/A
Sewerage and Sewage Treatment Implications		
<ul style="list-style-type: none"> Implementation of Sewer No. 1 and Sewer No.2 as proposed in Sections 7.2.2 - 7.2.3 of the EIA Report 	✓	✓

Waste Management – Recommended Mitigation Measures

Waste Management Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> Inert C&D materials (or public fills) will be used to form the ramps and other filling area as far as civil engineering design permits. 	✓	✓
<ul style="list-style-type: none"> The contractor should formulate waste management measures on waste minimization, storage, handling and disposal in a Waste Management Plan as part of Environmental Management Plan. 	✓	✓
<ul style="list-style-type: none"> Adopt good site practice as follows: <ul style="list-style-type: none"> Provide training to workers on site cleanliness, waste management (waste reduction, reuse and recycle) and chemical handling procedures Provide sufficient waste collection points and regular removal Cover waste materials with tarpaulin or in enclosure during transportation Maintain drainage systems, sumps and oil interceptors Sort out chemical waste for proper handling and treatment onsite or offsite 	P	P
<ul style="list-style-type: none"> Adopt waste reduction measures as follows: <ul style="list-style-type: none"> Allocate area/containers for sorting, recovering and storing waste for reuse, recycle or disposal (e.g. demolition debris and excavated materials, general refuse like aluminium cans.) Remove waste from the Site for sorting once generated if no suitable space can be identified. Allocate area for proper storage of construction materials to prevent contamination Minimize wastage through careful planning and avoiding over-purchase of construction materials 	P	✓
<ul style="list-style-type: none"> Store waste materials properly as follows: <ul style="list-style-type: none"> Avoid contamination by proper handling and storing waste Prevent erosion by covering waste Apply water spray on excavated materials Maintain and clean storage area regularly Sort and stockpile different materials at designated location to enhance reuse 	P	P
<ul style="list-style-type: none"> Apply for relevant waste disposal permits in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28), Dumping at Sea Ordinance (Cap. 466). 	✓	✓
<ul style="list-style-type: none"> Hire licensed waste disposal contractors for waste collection and removal. Dispose waste at licensed waste disposal facilities. 	✓	✓
<ul style="list-style-type: none"> Implement trip-ticket system for recording the amount of waste generated, recycled and disposed, including chemical wastes 	✓	✓
<ul style="list-style-type: none"> Reduce water content in wet spoil generated from piling work by mixing with dry materials. Only dispose treated spoil with less than 25% dry density to Public Fill Reception Facilities 	✓	✓

<ul style="list-style-type: none"> Dispose dry waste or waste with less than 70% water content by weight to landfill 	✓	✓
<ul style="list-style-type: none"> Follow the Code of Practice on the Packaging, Labelling and Storage of Chemical Waste as follows: <ul style="list-style-type: none"> Store chemical wastes with suitable containers. Seal and maintain the container to avoid leakage or spillage during storage, handling and transport Label chemical waste containers in both English and Chinese with instructions in accordance to Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation The container capacity should be smaller than 450 litres unless agreed by the EPD 	✓	✓
<ul style="list-style-type: none"> Comply with the requirement of the chemical storage area: <ul style="list-style-type: none"> Store only chemical waste and label clearly the chemical characters of the waste Have at least 3 sides enclosed and protected from rainfall with cover Provide sufficient ventilation Have impermeable floor and has bunds to contain 110% of the capacity of the largest container or 20% of the total volume of the stored waste in the area, whichever is larger Adequately spaced incompatible materials 	P	P
<ul style="list-style-type: none"> Transfer used lubricants, waste oils and other chemicals to oil recycling companies, if possible, and empty oil drums for reuse or refill. No direct or indirect discharge is permitted 	✓	✓
<ul style="list-style-type: none"> Hire licensed chemical waste disposal contractors for waste collection and removal. Dispose chemical waste at the approved Chemical Waste Treatment Centre at Tsing Yi or other licensed facility 	✓	✓
<ul style="list-style-type: none"> Hire reputable waste collector to separately collect and dispose general refuse from other wastes. Cover the waste to prevent being blown away 	✓	✓
<ul style="list-style-type: none"> The hauling of C&D materials shall follow established environmental mitigation measures as stated in Practice Note for Registered Contractors No. 17 "Control of Environmental Nuisance from Construction Sites" issued by the Buildings Department 	✓	✓
<ul style="list-style-type: none"> Provide recycling bins for sorting out recyclables for collection by recycling companies. Non-recyclables should be removed to designated landfills every day by licensed collectors to prevent environmental and health nuisance. 	✓	✓
<ul style="list-style-type: none"> Organize training and reminders to site staff on waste minimization through avoidance and reduction, reusing and recycling 	✓	✓
<ul style="list-style-type: none"> Bentonite slurry which will not be reused shall be disposed of from the Site as soon as possible. Residual used dewatered bentonite slurry should be disposed to a public filling area and liquid bentonite slurry if mixed with inert fill material should be disposed to a public filling area. 	N/A	N/A
<ul style="list-style-type: none"> If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the waste such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport the chemical wastes. The licensed collector shall deliver the waste to the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation 	✓	✓
<ul style="list-style-type: none"> Carry out weekly site inspection to check the implementation status of the recommended waste management measures. 	✓	✓
<ul style="list-style-type: none"> The barging of C&DM for this Project shall use the existing Kai Tak Barging Facility (KTBF), or otherwise approved by the Director. 	N/A	N/A

Ecology – Recommended Mitigation Measures

Ecology Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> Erection of hoarding, fencing or provision of clear demarcation of work zone 	✓	✓
<ul style="list-style-type: none"> Designate areas for placement of equipment, building materials and wastes away from drainage channels 	✓	✓

<ul style="list-style-type: none"> Carry out weekly site inspection to check the implementation status and the effectiveness of the proposed mitigation measures 	✓	✓
---	---	---

Landscape and Visual – Recommended Mitigation Measures

Landscape and Visual Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> Construction Lighting Control <ul style="list-style-type: none"> All security floodlights for construction sites should be equipped with adjustable shields, frosted diffusers and reflective covers, and be controlled to minimize light pollution and night-time glare to the visual sensitive receivers (VSRs). 	✓	N/A
<ul style="list-style-type: none"> Temporary Landscape Treatments <ul style="list-style-type: none"> Including vertical greening, pot planting and application of green roofing to site offices, Hydroseeding of site formation areas and short term greening of site boundaries and land not immediately developed. 	✓	N/A
<ul style="list-style-type: none"> Decoration of Hoarding <ul style="list-style-type: none"> Erection of screen hoardings should be designed appropriately to be compatible with the existing urban context, either brightly and imaginatively or with visually unobtrusive design and colours where more appropriate. 	✓	✓
<ul style="list-style-type: none"> All security floodlights for construction sites shall be equipped with adjustable shield, frosted diffusers and reflective covers, and be carefully controlled to minimize light pollution and night-time glare to nearby receivers 	✓	N/A
<ul style="list-style-type: none"> Site inspection should be undertaken once every two weeks. 	✓	✓
<ul style="list-style-type: none"> Compensatory Tree Planting <ul style="list-style-type: none"> A new parkland area is created in the project development to be used for the implementation of compensatory tree planting to offset the net loss of key landscape resources. It is recommended that 340 trees be planted in this regard and a compensatory tree planting proposal outlining the locations of tree compensation will be submitted separately in seeking relevant government department's approval in accordance with DEVB TC No.7/2015. 	N/A	N/A

Other – Recommended Mitigation Measures

<ul style="list-style-type: none"> Relevant environmental permits/licences should be posted at all vehicle entrances/exits. 	✓	P
--	---	---

Legend:

- ✓ Implemented
- × Not implemented
- P Partially implemented
- N/A Not applicable

Appendix J. Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

Table J.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Complaints	Notifications of Summons	Successful Prosecutions
This reporting period (Apr to Jun 2023)	3	0	0
From commencement date of construction to end of reporting month	29	0	0

Appendix K. Calibration Certificate



SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: HK2247804
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM 712, 7/F, MY LOFT 9 HOI WING ROAD, TUEN MUN, N.T., HK	SUB-BATCH	: 1
		DATE RECEIVED	: 30-NOV-2022
		DATE OF ISSUE	: 9-DEC-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
 - Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
 - Result(s) of sample(s) is/are reported on as received basis, unless otherwise specified.
 - Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.
-

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This report supersedes any previous report(s) with the same work order number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the **ALS Laboratory Group**

WORK ORDER : HK2247804
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ---



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2247804-001	S/N: 235780	Equipments	30-Nov-2022	S/N: 235780

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD – 3B
Serial No. 235780
Equipment Ref: NA
Job Order HK2247804

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 13 September 2022

Equipment Verification Results:

Verification Date: 6 December 2022


Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in $\mu\text{g}/\text{m}^3$ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01mins	09:37 ~ 11:38	17.1	1019.7	18.8	1451	12.0
2hr01mins	11:42 ~ 13:43	17.1	1019.7	20.7	1543	12.8
2hr01mins	13:48 ~ 15:49	17.1	1019.7	28.0	1605	13.3

Linear Regression of Y or X

Slope (K-factor): 1.8054 ($\mu\text{g}/\text{m}^3$)/CPM

Correlation Coefficient (R) 0.9651

Date of Issue 7 December 2022

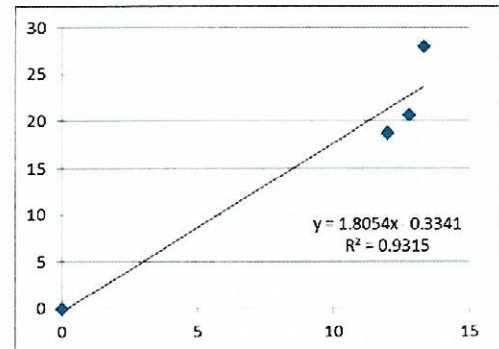

Remarks:

1. **Strong** Correlation ($R > 0.8$)
2. Factor 1.8054 ($\mu\text{g}/\text{m}^3$)/CPM should be applied for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

Operator: Fai So Signature:  Date: 7 December 2022

QC Reviewer: Ben Tam Signature:  Date: 7 December 2022



ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN
CLIENT : ENVIROTECH SERVICES CO.
ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD,
TUEN MUN, N.T. HONG KONG

WORK ORDER : **HK2208527**

SUB-BATCH : 1
DATE RECEIVED : 7-MAR-2022
DATE OF ISSUE : 15-MAR-2022

PROJECT : ---

NO. OF SAMPLES : 1
CLIENT ORDER : ---

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax +852 2610 2021 www.alsglobal.com

WORK ORDER : HK2208527
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2208527-001	S/N: 326285	Equipments	07-Mar-2022	S/N: 326285

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD – 3B
Serial No. 326285
Equipment Ref: NA
Job Order HK2208527

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 22 February 2022


Equipment Verification Results:

Verification Date: 8 March 2022

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01mins	09:31 ~ 11:32	19.5	1012.7	26.1	475	3.9
2hr01mins	11:34 ~ 13:35	19.5	1012.7	24.9	450	3.7
2hr03mins	13:37 ~ 15:40	19.5	1012.7	32.5	539	4.4

Linear Regression of Y or X

Slope (K-factor): 7.0384 (µg/m³)/CPM
Correlation Coefficient (R) 0.9947
Date of Issue 10 March 2022

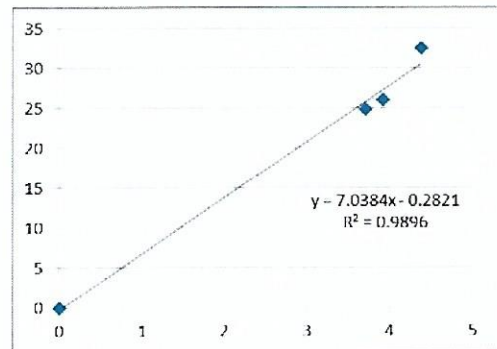

Remarks:

1. **Strong Correlation (R>0.8)**
2. Factor 7.0384 (µg/m³)/CPM should be applied for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : Martin Li Signature :  Date : 10 March 2022

QC Reviewer : Ben Tam Signature :  Date : 10 March 2022



SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: HK2241670
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM 712, 7/F, MY LOFT 9 HOI WING ROAD, TUEN MUN, N.T., HK	SUB-BATCH	: 1
		DATE RECEIVED	: 21-OCT-2022
		DATE OF ISSUE	: 1-NOV-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
 - Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
 - Result(s) of sample(s) is/are reported on as received basis, unless otherwise specified.
 - Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.
-

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the **ALS Laboratory Group**

WORK ORDER : HK2241670
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ---



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2241670-001	S/N: 436553	Equipments	21-Oct-2022	S/N: 436553

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD – 3B
Serial No. 436553
Equipment Ref: NA
Job Order HK2241670

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 13 September 2022

Equipment Verification Results:

Verification Date: 25 October 2022

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in $\mu\text{g}/\text{m}^3$ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01mins	09:20 ~ 11:21	23.8	1018.2	33.7	2401	19.9
2hr02mins	11:23 ~ 13:25	23.8	1018.2	27.9	2303	18.9
2hr04mins	13:27 ~ 15:31	23.8	1018.2	43.6	2703	21.9

Linear Regression of Y or X

Slope (K-factor): 1.7854 ($\mu\text{g}/\text{m}^3$)/CPM


Correlation Coefficient (R) 0.9729

Date of Issue 26 October 2022


Remarks:

1. **Strong Correlation** ($R > 0.8$)
2. Factor 1.7854 ($\mu\text{g}/\text{m}^3$)/CPM should be applied for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

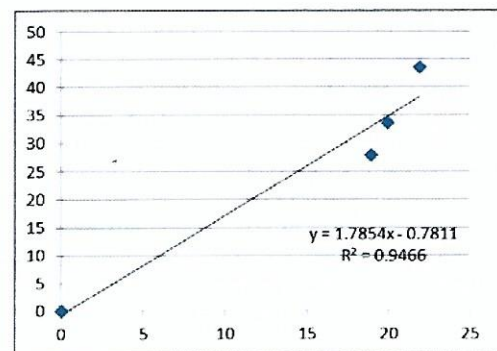

Operator : Fai So Signature :  Date : 26 October 2022

QC Reviewer : Ben Tam Signature :  Date : 26 October 2022



ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: HK2219477
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM 712, 7/F, MY LOFT 9 HOI WING ROAD, TUEN MUN, N.T., HK	SUB-BATCH	: 1
		DATE RECEIVED	: 26-MAY-2022
		DATE OF ISSUE	: 7-JUN-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Kwai Tsing Hong Kong

WORK ORDER : HK2219477
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ---



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2219477-001	S/N: 456668	Equipments	26-May-2022	S/N: 456668

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD – 3B
Serial No. 456668
Equipment Ref: NA
Job Order HK2219477

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 27 May 2022

Equipment Verification Results:

Verification Date: 27 May 2022


Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in $\mu\text{g}/\text{m}^3$ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01mins	09:27 ~ 11:28	27.4	1004.3	38.0	1735	14.4
2hr01mins	11:32 ~ 13:33	27.4	1004.3	30.3	1585	13.1
2hr	13:37 ~ 15:37	27.4	1004.3	34.1	1712	14.3

Linear Regression of Y or X

Slope (K-factor): 2.4695 ($\mu\text{g}/\text{m}^3$)/CPM

Correlation Coefficient (R) 0.9938

Date of Issue 2 June 2022

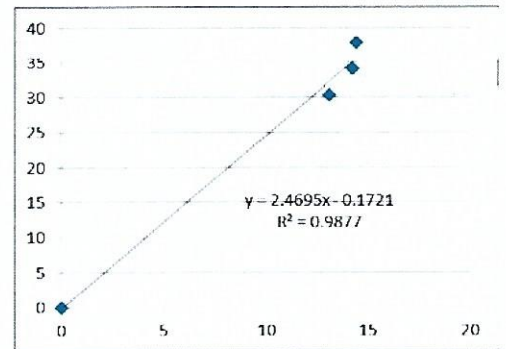

Remarks:

1. **Strong Correlation ($R > 0.8$)**
2. Factor 2.4695 ($\mu\text{g}/\text{m}^3$)/CPM should be applied for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

Operator : Fai So Signature :  Date : 2 June 2022

QC Reviewer : Ben Tam Signature :  Date : 2 June 2022



ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: HK2219480
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM 712, 7/F, MY LOFT 9 HOI WING ROAD, TUEN MUN, N.T., HK	SUB-BATCH	: 1
		DATE RECEIVED	: 26-MAY-2022
		DATE OF ISSUE	: 7-JUN-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action-United Environmental Services & Consulting.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Kwai Tsing Hong Kong

WORK ORDER : HK2219480
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2219480-001	S/N: 476664	Equipments	26-May-2022	S/N: 476664

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
 Manufacturer: Sibata LD – 3B
 Serial No. 476664
 Equipment Ref: NA
 Job Order HK2219480

Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)
 Location & Location ID: AUES office (calibration room)
 Equipment Ref: HVS 018
 Last Calibration Date: 27 May 2022


Equipment Verification Results:

Verification Date: 27 May 2022

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in $\mu\text{g}/\text{m}^3$ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01mins	09:27 ~ 11:28	27.4	1004.3	38.0	1779	14.8
2hr01mins	11:32 ~ 13:33	27.4	1004.3	30.3	1727	14.2
2hr	13:37 ~ 15:37	27.4	1004.3	34.1	1751	14.6

Linear Regression of Y or X

Slope (K-factor): 2.3584 ($\mu\text{g}/\text{m}^3$)/CPM
 Correlation Coefficient (R) 0.9883
 Date of Issue 2 June 2022

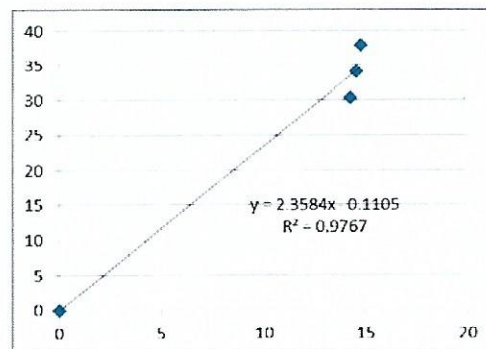

Remarks:

1. **Strong** Correlation ($R > 0.8$)
2. Factor 2.3584 ($\mu\text{g}/\text{m}^3$)/CPM should be applied for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

Operator : Fai So Signature : *Fai So* Date : 2 June 2022

QC Reviewer : Ben Tam Signature : *Ben Tam* Date : 2 June 2022



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C224774
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC22-1518)

Date of Receipt / 收件日期 : 1 August 2022

Description / 儀器名稱 : Precision Acoustic Calibrator

Manufacturer / 製造商 : LARSON DAVIS

Model No. / 型號 : CAL200

Serial No. / 編號 : 16878

Supplied By / 委託者 : Envirotech Services Co.

Room 712, 7/F, My Loft, 9 Hoi Wing Road, Tuen Mun,
New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 20 August 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By

測試

:

H T Wong

Assistant Engineer

Certified By

核證

:

K C Lee

Engineer

Date of Issue

簽發日期

:

23 August 2022

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C224774

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C223647
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C221705

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.9	± 0.2	± 0.2
114 dB, 1 kHz	113.9		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate of Calibration

校正證書

Certificate No. : C224775

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC22-1518)

Date of Receipt / 收件日期 : 1 August 2022

Description / 儀器名稱 : Sound Level Meter

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00643040

Supplied By / 委託者 : Envirotech Services Co.

Room 712, 7/F, My Loft, 9 Hoi Wing Road, Tuen Mun,
New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 20 August 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By
測試

:



H T Wong
Assistant Engineer

Certified By
核證

:



K C Lee
Engineer

Date of Issue

:

23 August 2022

簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C224775

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C220381
CL281	Multifunction Acoustic Calibrator	AV210017

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.3	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	94.3 (Ref.)
				104.00		104.5
				114.00		114.6

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.3	Ref.
			Slow			94.3	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C224775
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting


UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _A	A	Fast	94.00	63 Hz	68.1	-26.2 ± 1.5
					125 Hz	78.1	-16.1 ± 1.5
					250 Hz	85.6	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.3	Ref.
					2 kHz	95.5	+1.2 ± 1.6
					4 kHz	95.3	+1.0 ± 1.6
					8 kHz	93.3	-1.1 (+2.1 ; -3.1)
					16 kHz	86.3	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _C	C	Fast	94.00	63 Hz	93.4	-0.8 ± 1.5
					125 Hz	94.1	-0.2 ± 1.5
					250 Hz	94.3	0.0 ± 1.4
					500 Hz	94.3	0.0 ± 1.4
					1 kHz	94.3	Ref.
					2 kHz	94.1	-0.2 ± 1.6
					4 kHz	93.5	-0.8 ± 1.6
					8 kHz	91.4	-3.0 (+2.1 ; -3.1)
					16 kHz	84.4	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C224775

證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 10446

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Appendix L. Complaint Investigation Report

Complaint Investigation Report

RECEIPT OF COMPLAINT		Ref: COM_0027
Date:	25 April 2023	
Time:	12:09	
From:	public complaint referred by EPD (EPD Ref.: K19/RE/00009561-23 and K19/RE/00009572-23)	
Via:	email by contractor representative	
Contact no.:	-	
COMPLAINANT		
Name:	-	Address: -
Contact no.:	-	
DETAILS OF COMPLAINT		
Date:	16 April 2023	
Time:	-	
Parameter:*	Dust Noise Water Other (specify):	
Description:	<p>- Complaint of construction noise from the construction site of Kai Tak Sports Park in the night time (around 20:xx) on 13/4/2023 and 15/4/2023.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	
INVESTIGATION RESULT & RESPONSE		
ET, IEC and SOR notified on:	25 April 2023	
Investigation conducted on:	25 April 2023	
Result of investigation:	<p>Complaint investigation was carried out with contractor on 27 April 2023, the results of investigation were summarized as following:</p> <p>According to the contractor information, no construction work were scheduled between 19:00-07:00 on complaint dates (i.e. 13/4/2023 and 15/4/2023). No construction activities were scheduled at night-time in April 2023. All construction works carried out on site have been strictly followed the Construction Noise Permit requirement. The CNP for the construction works at southern site (site area closest to the Grand Waterfront) is attached for information.</p> <p>ET and contractor carried out regular site inspections at Kai Tak Sports Park on 12 April 2023. (Photo 1) Noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule were generally implemented during the time of inspection.</p> <p>According to the contractor information, noise mitigation control measures maintained on site included:</p> <ol style="list-style-type: none"> 1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents (photo 2). <p>In conclusion, noise control mitigation measures at the Kai Tak Sports Park have been implemented and maintained. All construction works carried out have been fulfilling the relevant environmental legislations and CNP requirement during the concerned period.</p>	

RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS

Environmental mitigation measures have been maintained as follow:

1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents (photo 2)
2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. (Photo 3)
3. Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement. (Photo 4)
4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule.

Prepared by: Sunny Chan Title: Environmental Team Leader

Signature:  Date: 28 April 2023

Attachment:

1. Record of Construction Noise Permit - GW-RE1157-22
2. Photo Records

本署檔案
OUR REF : (4) in EP631/K19/RE485202-22
來函檔案
YOUR REF :
電話
TEL NO : 2150 8081
圖文傳真
FAX NO : 2402 8275
網址
HOMEPAGE : <http://www.epd.gov.hk/>

Environmental Protection Department
Environmental Compliance Division
Regional Office (East)
8/F., Cheung Sha Wan Government Offices,
303 Cheung Sha Wan Road,
Kowloon



環境保護署
環保法規管理科
區域辦事處(東)
九龍長沙灣道 303 號
長沙灣政府合署 8 樓

Registered Post

28 October 2022

To: HIP HING ENGINEERING COMPANY LIMITED
11/F., Chevalier Commercial Centre,
8 Wang Hoi Road,
Kowloon Bay,
Kowloon

Dear Sir,


**Notice of Issue of Construction Noise Permit pursuant
to section 8(6) of the Noise Control Ordinance (Cap. 400)**

I write to inform you that, under section 8(6) of the Noise Control Ordinance, the Authority has decided to issue a construction noise permit in respect of your application, which was received by the Authority on 11 October 2022, **for the use of powered mechanical equipment for carrying out construction work at Construction site of Kai Tak Sports Park (South), Kai Tak, Kowloon.**

The construction noise permit No. GW-RE1157-22 is enclosed.

You are advised to read the conditions of the permit carefully and to ensure compliance with these conditions. Any breaching of the conditions may lead to cancellation of the permit, **subsequent prosecution action** and the Authority's refusal to issue further permit for the above construction site.

Yours faithfully,


(LEONG Ka-long, Karen)
for Authority

Note:

Electronic submission of application for construction noise permit is available at Environmental Protection Department's website. File attachments with total size not exceeding 20 MB in acceptable format are allowed for electronic submission. Electronic application form can be downloaded from our website (<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>) and an overview of application submission (<https://epic.epd.gov.hk/eForm/introduce.html>) is provided for more information.

(4) in EP631/K19/RE485202-22

2150 8081

2402 8275

掛號函件

致： 九龍 九龍灣
宏開道 8 號
其士商業中心 11 樓
協興工程有限公司

執事先生：

根據《噪音管制條例(第 400 章)》第 8(6)條
發出的通知書 — 簽發「建築噪音許可證」

本監督於二零二二年十月十一日，收到你擬於下述地址：九龍啟德啟德體育園(南)的建築地盤，使用機動設備進行建築工程而提出的「建築噪音許可證」申請，現根據《噪音管制條例》第 8(6)條的規定通知你，上述的申請已被批准。

隨函附上「第 GW-RE1157-22 號建築噪音許可證」。

請細閱許可證各項條件，確保遵守，如有違反，本監督可撤銷許可證，提出檢控及拒絕再就上述地盤簽發任何「建築噪音許可證」。

監 督

(梁嘉朗



代行)

二零二二年十月二十八日

注意：

環境保護署提供網上申請「建築噪音許可證」服務。網上申請容許上傳檔案總容量不大於 20 MB 的有關文件。可於本署網頁下載電子表格

(<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>)

及參閱電子表格提交服務概覽(<https://epic.epd.gov.hk/eForm/introduce.html>)，了解更多資料。

FORM 3
NOISE CONTROL ORDINANCE
(Chapter 400)
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE1157-22

To : HIP HING ENGINEERING COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed :

Full address : Construction site of Kai Tak Sports Park (South), Kai Tak, Kowloon.

Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. * PART/WHOLE of the site falls * WITHIN/OUTSIDE a designated area.

3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
	Refer to attached sheet	

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 25 November 2022 at 0000 hours
Days and hours : 0000-2400 hours on general holiday (including Sunday), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday [but note condition 3.d.1. below for the operating hours within which the use of the above listed powered mechanical equipment is allowed].

This part of the permit expires on : 23 May 2023 at 2400 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.

- d. Other conditions imposed on the use of the powered mechanical equipment:

Refer to attached sheet.

4. Prescribed Construction Work

a. Type of prescribed construction work which may be carried out inside the site boundary :

<i>Identification code of type of prescribed construction work</i>	<i>Description of type of prescribed construction work</i>
	Not applicable

b. Validity of the construction noise permit for the carrying out of the prescribed construction work:

Date and time of commencement: Not applicable at Not applicable

Days and hours: Not applicable

This part of the permit expires on : Not applicable at Not applicable


c. ~~Site layout plan(s), endorsed by the Authority, may be attached with the permit to indicate the locations permitted for the carrying out of prescribed construction work described in this permit. The layout plan(s) is(are) required to be kept on the construction site and made available for inspection by the Authority.~~

d. Other conditions imposed on the carrying out of the prescribed construction work:

5. This construction noise permit or a copy thereof must be displayed on the construction site at all vehicular entrances for public information.

Dated this 28th day of October 20 22

Signed : _____


 (LEONG Ka-long, Karen)
 for Authority

* Delete as necessary

表格 3
 噪音管制條例
 (第400章)
 第8(9)條

建築噪音許可證
 為進行建築工程(撞擊式打樁除外)
 而使用機動設備及/或進行訂明建築工程

建築噪音許可證編號： GW-RE1157-22

致： 協興工程有限公司

本建築噪音許可證是按照《噪音管制條例》第8條的規定而發出的。現准予使用機動設備以進行撞擊式打樁工程以外的建築工程及/或進行訂明建築工程，但須受以下條件規限。若不按照該等條件進行建築工程，許可證可遭撤銷，而且會受到檢控。

條 件

1. 可使用機動設備及/或進行訂明建築工程的建築地盤：

詳細地址：九龍啟德啟德體育園(南)的建築地盤。

地段編號：---

地盤範圍(即可使用機動設備及進行訂明建築工程的地方範圍)已描劃於夾附的圖則上，而該圖則是本建築噪音許可證的一部分。

2. 該地盤部分/全部*位於指定範圍之內/外*。

3. 機動設備

- a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)	各項機動設備的說明	數目
	參見附頁。	

- b. 可使用機動設備的建築噪音許可證有效期：

生效日期及時間：二零二二年十一月二十五日 凌晨零時

日期及時間：公眾假日(包括星期日)的凌晨零時至晚上十二時，公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時【但須注意條件3.d.1.有關可以使用上列機動設備的時間】。

此部分許可證屆滿日期及時間：二零二三年五月二十三日 晚上十二時
 日期 時間

- c. 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各一幀，供監督隨時查看；該等照片須經監督認可。

- d. 規限使用機動設備的其他條件：

參見附頁。

4. 訂明建築工程

a. 在地盤範圍內可進行的訂明建築工程：

訂明建築工程的識辨代碼	訂明建築工程的類別的說明
	不適用

b. 可進行訂明建築工程的建築噪音許可證有效期：

生效日期及時間： 不適用

日期及時間： 不適用。

此部分許可證屆滿日期及時間： 不適用

日期 時間

c. 本許可證可夾附經監督認可的地盤圖則，以顯示本許可證准予進行訂明建築工程的地點。該地盤圖則須存放於建築地盤供監督隨時查看。

d. 規限進行訂明建築工程的其他條件：

5. 本建築噪音許可證或其副本必須展示於建築地盤的所有車輛入口處，給予公眾人士參閱。

日期：20 22 年 10 月 28 日



簽署： _____

監督
(梁嘉朗 代行)


* 刪去不適用者

Sheet Attached to Construction Noise Permit

No. GW-RE1157-22

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
Group A CNP 049	Crane, tower (electric)	Five
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	Five
---	Agitator (electric)	One
CNP 021	Bar bender and cutter (electric)	One
---	Water jetting unit (electric)	One
Group B CNP 049	Crane, tower (electric)	Six
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	Six
Group C ---	Welding machine (electric)	Ten
CNP 122	Hoist, passenger/material (electric)	Six
---	Pallet truck (electric)	One
---	Air blower (electric)	Three
---	Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 103 dB(A)	One
Group D ---	Lorry, with crane, 5.5 tonne < gross vehicle weight ≤ 38 tonne <u>OR</u>	One
---	Lorry, 5.5 tonne < gross vehicle weight ≤ 38 tonne	

Signed : 
 (LEONG Ka-long, Karen)
 for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3.a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)		各項機動設備的說明	數目
<u>A 組</u>	CNP 049	起重機，塔型 (電動)	伍
	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	伍
	---	攪動機 (電動)	壹
	CNP 021	鋼筋彎曲機及切割機 (電動)	壹
	---	噴水機 (電動)	壹
<u>B 組</u>	CNP 049	起重機，塔型 (電動)	陸
	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	陸
<u>C 組</u>	---	焊接機 (電動)	拾
	CNP 122	吊機，乘客/物料 (電動)	陸
	---	托盤車 (電動)	壹
	---	吹風機 (電動)	叁
	---	起重機，流動 (油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 103 分貝(A)	壹
<u>D 組</u>	---	吊臂貨車，5.5 噸 < 總重量 ≤ 38 噸 或	壹
	---	貨車，5.5 噸 < 總重量 ≤ 38 噸	



簽署：_____

監督
(梁嘉朗 代行)


Sheet Attached to Construction Noise Permit

No. GW-RE1157-22

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

Identification code of item of powered mechanical equipment (if applicable)	Description of item of powered mechanical equipment	No. of units
Group E CNP 049	Crane, tower (electric)	One
---	Chain hoist (electric) OR	One
---	Gondola (electric)	
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	One
CNP 283	Water pump, submersible (electric)	Ten
---	Lorry, with crane, 5.5 tonne < gross vehicle weight ≤ 38 tonne OR	One
---	Lorry, 5.5 tonne < gross vehicle weight ≤ 38 tonne	
---	Welding machine (electric)	Twenty-eight
Group F ---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	Four
CNP 283	Water pump, submersible (electric)	Ten
Group G ---	Concrete lorry mixer (Vehicle No. SR7648 OR KK8459 OR SK9032 OR UX3079 OR LP129 OR UW6149 OR UB4513 OR RG3200 OR TX2593 OR RN6493 OR UC2932 OR TW4381 OR TT3797 OR TU4368 OR SB9550 OR TT3923 OR TU1786 OR PR3797 OR TG4819 OR TU1097 OR RW5108 OR TT3231 OR SD1890 OR TW5863 OR TG5625)	One
---	Concrete pump, lorry mounted (Model No. 56X-6RZ / Serial No. ZLJ5430THBK)	One
Group H ---	Poker, vibratory, hand-held (electric)	One

Signed :


 (LEONG Ka-long, Katen)
 for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3.a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)		各項機動設備的說明	數目
<u>E 組</u>	CNP 049	起重機，塔型 (電動)	壹
	---	鏈型吊機 (電動) 或	壹
	---	吊船 (電動)	
	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	壹
	CNP 283	潛水泵 (電動)	拾
	---	吊臂貨車，5.5 噸 < 總重量 ≤ 38 噸 或	壹
	---	貨車，5.5 噸 < 總重量 ≤ 38 噸	
	---	焊接機 (電動)	貳拾捌
<u>F 組</u>	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	肆
	CNP 283	潛水泵 (電動)	拾
<u>G 組</u>	---	混凝土攪拌車 (車牌號碼 SR7648 或 KK8459 或 SK9032 或 UX3079 或 LP129 或 UW6149 或 UB4513 或 RG3200 或 TX2593 或 RN6493 或 UC2932 或 TW4381 或 TT3797 或 TU4368 或 SB9550 或 TT3923 或 TU1786 或 PR3797 或 TG4819 或 TU1097 或 RW5108 或 TT3231 或 SD1890 或 TW5863 或 TG5625)	壹
	---	混凝土泵，裝在貨車上 (型號 56X-6RZ / 序號 ZLJ5430THBK)	壹
<u>H 組</u>	---	混凝土震動機，手提型 (電動)	壹



簽署：_____

監督
(梁嘉朗 代行)

Sheet Attached to Construction Noise Permit

No. GW-RE1157-22

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
<u>Group I</u> CNP 049 --- --- --- --- CNP 283 CNP 065	Crane, tower (electric) Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A) Air blower (electric) Scissor lifting platform <u>OR</u> Cherry picker Water pump, submersible (electric) Drill / Grinder, hand-held (electric)	Two Two Two Three Three Two
<u>Group J</u> --- --- --- CNP 283 --- --- ---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A) Air blower (electric) Grout pump Water pump, submersible (electric) Welding machine (electric) Grout mixer <u>OR</u> Mixer, hand-held (electric)	One One One Five Ten One
<u>Group K</u> --- --- ---	Dump truck, 5.5 tonne < gross vehicle weight ≤ 38 tonne <u>OR</u> Dump truck, with grab, 5.5 tonne < gross vehicle weight ≤ 38 tonne Excavator, tracked, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 92 dB(A)	One Two
<u>Group L</u> ---	Forklift	One
<u>Group M</u> CNP 066	Dumper	One

Signed : 
(LEONG Ka-long, Karen)
for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3.a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)		各項機動設備的說明	數目
<u>I組</u>	CNP 049	起重機，塔型(電動)	貳
	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	貳
	---	吹風機(電動)	貳
	---	鉸剪式升降台 或	叁
	---	升降台	叁
	CNP 283	潛水泵(電動)	叁
	CNP 065	鑽 / 磨機，手提型(電動)	貳
<u>J組</u>	---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	壹
	---	吹風機(電動)	壹
	---	灌漿泵	壹
	CNP 283	潛水泵(電動)	伍
	---	焊接機(電動)	拾
	---	灌漿攪拌機 或	壹
	---	攪拌機，手提型(電動)	壹
<u>K組</u>	---	卸土車，5.5噸<總重量 ≤ 38 噸 或	壹
	---	抓斗卸土車，5.5噸<總重量 ≤ 38 噸	壹
	---	挖土機，履帶式，備有優質機動設備標籤顯示聲功率級 ≤ 92 分貝(A)	貳
<u>L組</u>	---	鏟車	壹
<u>M組</u>	CNP 066	卸土機	壹



簽署：_____

監督

(梁嘉朗 代行)


Sheet Attached to Construction Noise Permit

No. GW-RE1157-22

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
<u>Group N</u> ---	Welding machine (electric)	Six
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	One
---	Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 103 dB(A)	Two
<u>Group O</u> ---	Air compressor, with Noise Emission Label showing a Sound Power Level ≤ 97 dB(A)	One
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	One
---	Needle scaler (pneumatic)	Two
<u>Group P</u> ---	Welding machine (electric)	Eight
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	One
---	Air blower (electric)	One
---	Scissor lifting platform <u>OR</u>	Four
---	Cherry picker	Four
CNP 065	Drill / Grinder, hand-held (electric)	Four
<u>Group Q</u> ---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 97 dB(A)	Two
CNP 283	Water pump, submersible (electric)	Two
CNP 065	Drill / Grinder, hand-held (electric)	Six
<u>Group R</u> ---	Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 103 dB(A)	One
---	Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 102 dB(A)	One

Signed :



(LEONG Ka-long, Karen)
for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3.a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)	各項機動設備的說明	數目
<u>N組</u> ---	焊接機(電動)	陸
---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	壹
---	起重機，流動(油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 103 分貝(A)	貳
<u>O組</u> ---	空氣壓縮機，備有噪音標籤顯示聲功率級 ≤ 97 分貝(A)	壹
---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	壹
---	針束除銹機(氣動)	貳
<u>P組</u> ---	焊接機(電動)	捌
---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	壹
---	吹風機(電動)	壹
---	鉸剪式升降台 或	肆
---	升降台	肆
CNP 065	鑽 / 磨機，手提型(電動)	肆
<u>Q組</u> ---	發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)	貳
CNP 283	潛水泵(電動)	貳
CNP 065	鑽 / 磨機，手提型(電動)	陸
<u>R組</u> ---	起重機，流動(油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 103 分貝(A)	壹
---	起重機，流動(油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 102 分貝(A)	壹



簽署：_____

監督

(梁嘉朗 代行)


Sheet Attached to Construction Noise Permit

No. GW-RE1157-22

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
<u>Group S</u> CNP 065	Drill / Grinder, hand-held (electric)	Seven
<u>Group T</u> ---	Wrench, torque (electric)	One
<u>Group U</u> ---	Breaker, hand-held (electric), with Noise Emission Label showing a Sound Power Level ≤ 105 dB(A)	One
<u>Group V</u> CNP 283	Water pump, submersible (electric)	Two
---	Welding machine (electric)	Two
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level ≤ 87 dB(A)	One

Signed :



(LEONG Ka-long, Karen)
for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3.a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)		各項機動設備的說明	數目
<u>S</u> 組	CNP 065	鑽 / 磨機，手提型 (電動)	柒
<u>T</u> 組	---	扭力扳手 (電動)	壹
<u>U</u> 組	---	破碎機，手提型 (電動)，備有噪音標籤顯示聲功率級 \leq 105 分貝(A)	壹
<u>V</u> 組	CNP 283	潛水泵 (電動)	貳
	---	焊接機 (電動)	貳
	---	發電機，備有優質機動設備標籤顯示聲功率級 \leq 87 分貝(A)	壹



簽署：_____

監督
(梁嘉朗 代行)

Sheet Attached to Construction Noise Permit
No. GW-RE1157-22


3.d. Other conditions imposed on the use of the powered mechanical equipment:

1. The powered mechanical equipment listed in condition 3.a. shall only be operated during the hours shown below:

<u>Group A – U</u>	General holiday including Sunday	0700 – 2300 hours
	Any day not being a general holiday	1900 – 2300 hours
<u>Group V</u>	Any day	2300 – 0700 hours on next day

2. Only one group of the powered mechanical equipment listed in condition 3.a. shall be allowed to operate at any time.
3. The powered mechanical equipment covered by this Construction Noise Permit shall not be operated when any powered mechanical equipment covered by the Construction Noise Permit No. GW-RE0978-22 is being operated.

Signed : _____


(LEONG Ka-long, Karen)
for Authority

建築噪音許可證
編號 GW-RE1157-22 的附頁

3. d. 規限使用機動設備的其他條件：

1. 祇可於以下時間內使用列在條件 3. a. 內的機動設備：

<u>A 至 U 組</u>	公眾假日包括星期日	上午七時 至 晚上十一時
	公眾假日以外的任何一日	下午七時 至 晚上十一時
<u>V 組</u>	任何一日	晚上十一時至翌日上午七時

2. 在任何時間內，祇可使用列在條件 3. a. 內的其中一組機動設備。
3. 當建築噪音許可證編號 GW-RE0978-22 內的任何機動設備正在操作時，不可操作本建築噪音許可證內的機動設備。



簽署：_____

監督

(梁嘉朗 代行)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



CNP 283 Water pump, submersible (electric)
潛水泵 (電動)



Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label
showing a Sound Power Level ≤ 103 dB(A)

起重機，流動 (油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 103 分貝(A)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Generator, with Quality Powered Mechanical Equipment Label showing
a Sound Power Level ≤ 87 dB(A)

發電機，備有優質機動設備標籤顯示聲功率級 ≤ 87 分貝(A)




Generator, with Quality Powered Mechanical Equipment Label showing
a Sound Power Level ≤ 97 dB(A)


發電機，備有優質機動設備標籤顯示聲功率級 ≤ 97 分貝(A)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片

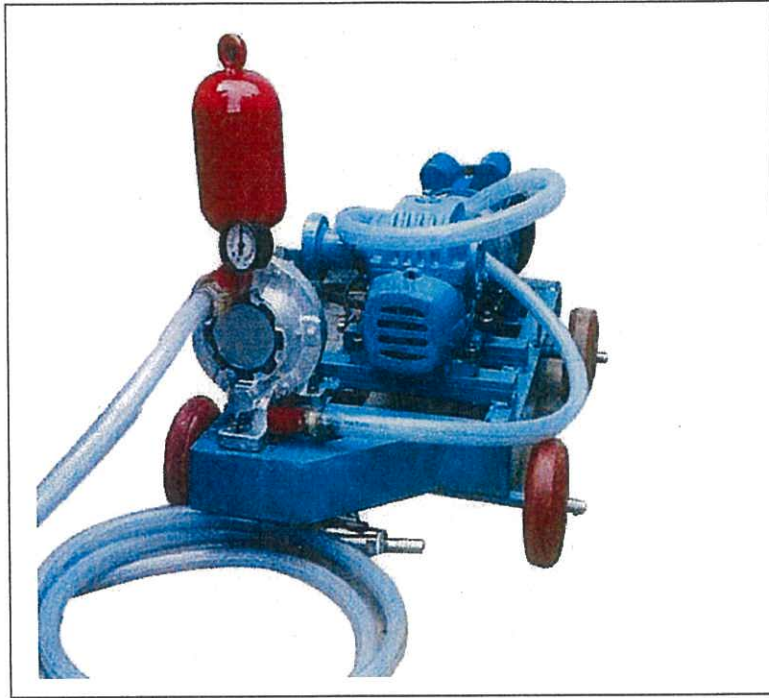

Grout pump
灌漿泵

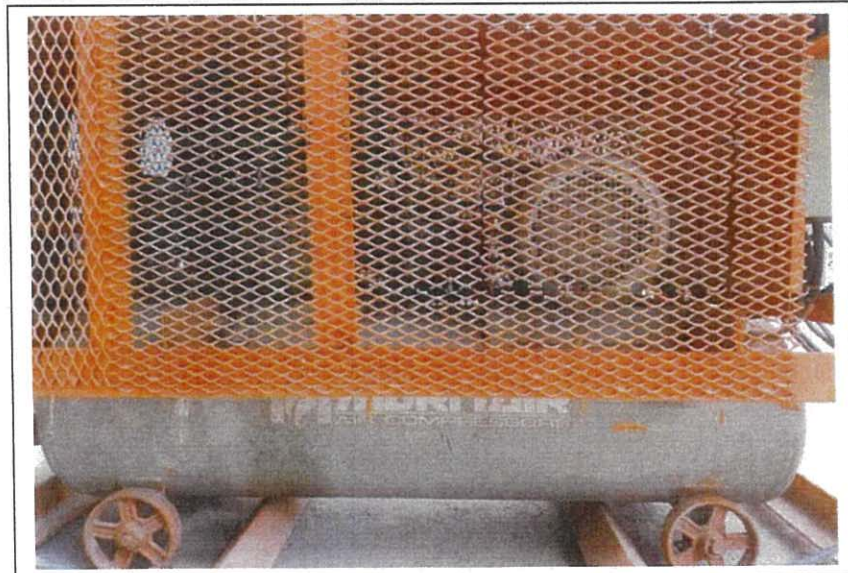

Air compressor, with Noise Emission Label showing a Sound Power Level ≤ 97 dB(A)

空氣壓縮機，備有噪音標籤顯示聲功率級 ≤ 97 分貝(A)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Grout mixer
灌漿攪拌機



Lorry, with crane, 5.5 tonne < gross vehicle weight \leq 38 tonne
吊臂貨車，5.5 噸 < 總重量 \leq 38 噸



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Lorry, 5.5 tonne < gross vehicle weight \leq 38 tonne
貨車，5.5 噸 < 總重量 \leq 38 噸



Welding machine (electric)
焊接機 (電動)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



CNP 021 Bar bender and cutter (electric)
鋼筋彎曲機及切割機 (電動)



CNP 049 Crane, tower (electric)
起重機，塔型 (電動)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



CNP 065 Drill, hand-held (electric)
鑽，手提型（電動）



CNP 065 Grinder, hand-held (electric)
磨機，手提型（電動）



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Excavator, tracked, with Quality Powered Mechanical Equipment Label
showing a Sound Power Level ≤ 92 dB(A)
挖土機，履帶式，備有優質機動設備標籤顯示聲功率級 ≤ 92 分貝(A)



Dump truck, with grab, 5.5 tonne < gross vehicle weight ≤ 38 tonne
抓斗卸土車，5.5 噸 < 總重量 ≤ 38 噸



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Dump truck, 5.5 tonne < gross vehicle weight \leq 38 tonne
卸土車，5.5 噸 < 總重量 \leq 38 噸




Water jetting unit (electric)
噴水機 (電動)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Air blower (electric)
吹風機 (電動)

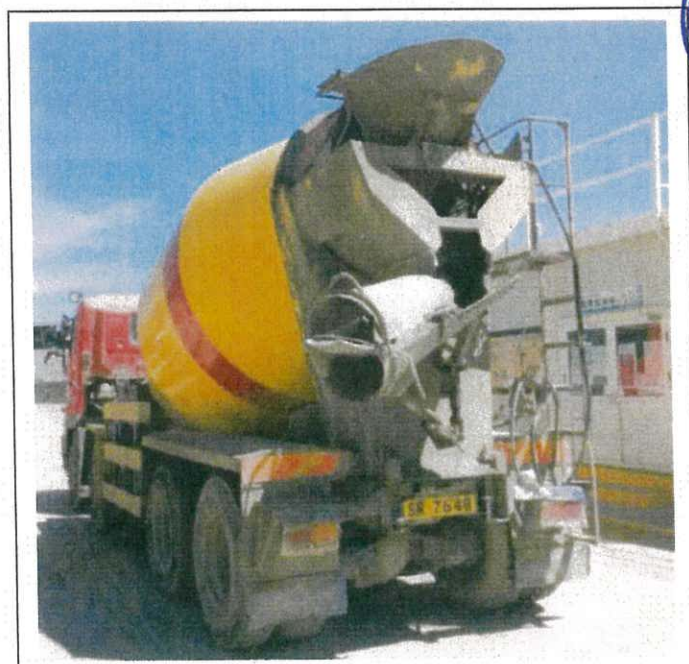

Concrete lorry mixer (Vehicle No. SR7648)
混凝土攪拌車 (車牌號碼 SR7648)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. KK8459)
混凝土攪拌車 (車牌號碼 KK8459)




Concrete lorry mixer (Vehicle No. SK9032)
混凝土攪拌車 (車牌號碼 SK9032)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片




Concrete lorry mixer (Vehicle No. UX3079)
混凝土攪拌車 (車牌號碼 UX3079)

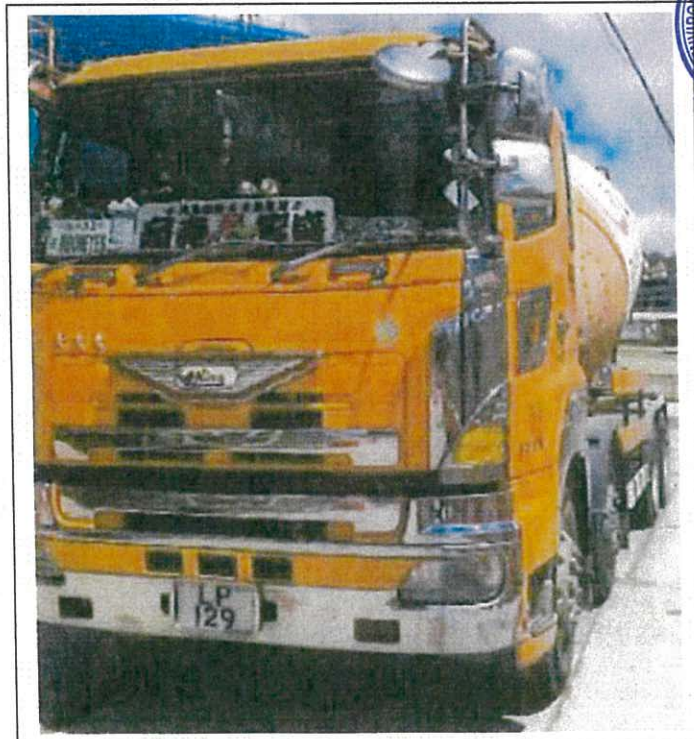

Concrete lorry mixer (Vehicle No. LP129)
混凝土攪拌車 (車牌號碼 LP129)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片

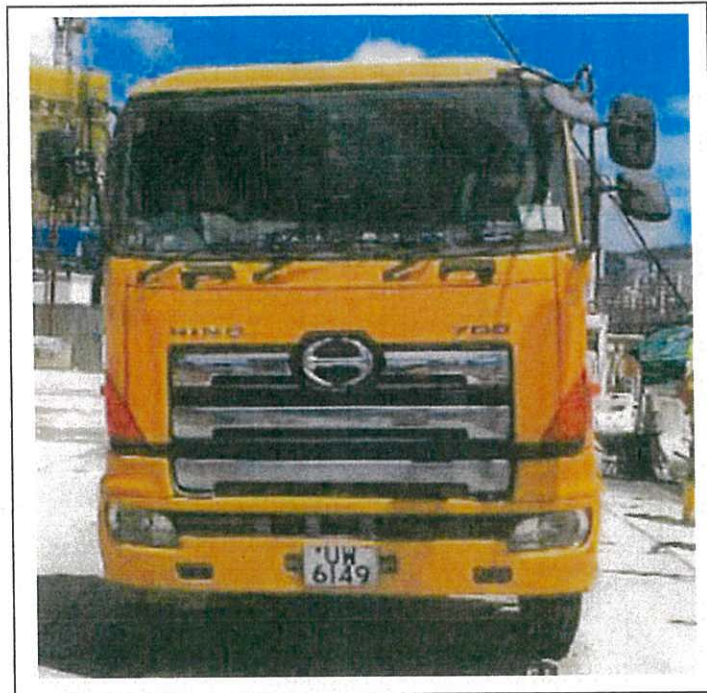

Concrete lorry mixer (Vehicle No. UW6149)
混凝土攪拌車 (車牌號碼 UW6149)




Concrete lorry mixer (Vehicle No. UB4513)
混凝土攪拌車 (車牌號碼 UB4513)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. RG3200)
混凝土攪拌車 (車牌號碼 RG3200)

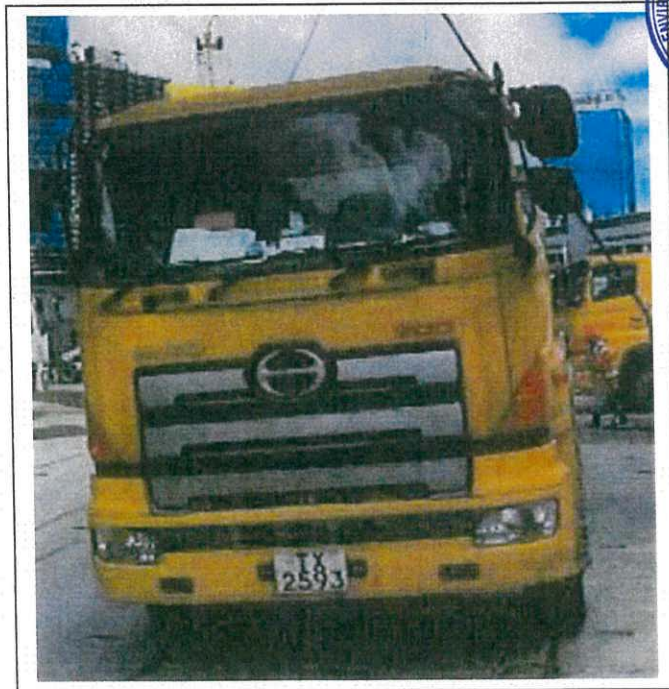

Concrete lorry mixer (Vehicle No. TX2593)
混凝土攪拌車 (車牌號碼 TX2593)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. RN6493)
混凝土攪拌車 (車牌號碼 RN6493)



Concrete lorry mixer (Vehicle No. UC2932)
混凝土攪拌車 (車牌號碼 UC2932)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片




Concrete lorry mixer (Vehicle No. TW4381)
混凝土攪拌車 (車牌號碼 TW4381)



Concrete lorry mixer (Vehicle No. TT3797)
混凝土攪拌車 (車牌號碼 TT3797)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片

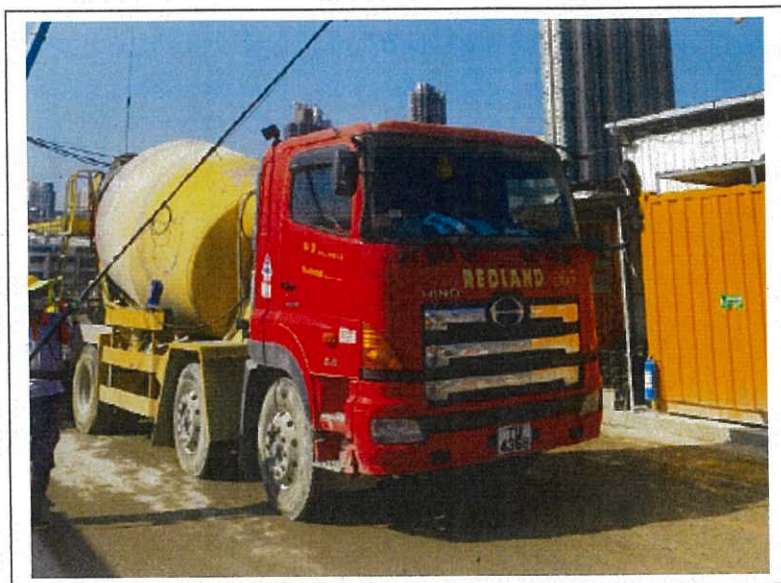

Concrete lorry mixer (Vehicle No. TU4368)
混凝土攪拌車 (車牌號碼 TU4368)



Concrete lorry mixer (Vehicle No. SB9550)
混凝土攪拌車 (車牌號碼 SB9550)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. TT3923)
混凝土攪拌車 (車牌號碼 TT3923)



Concrete lorry mixer (Vehicle No. TU1786)
混凝土攪拌車 (車牌號碼 TU1786)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. PR3797)
混凝土攪拌車 (車牌號碼 PR3797)




Concrete lorry mixer (Vehicle No. TG4819)
混凝土攪拌車 (車牌號碼 TG4819)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. TU1097)
混凝土攪拌車 (車牌號碼 TU1097)

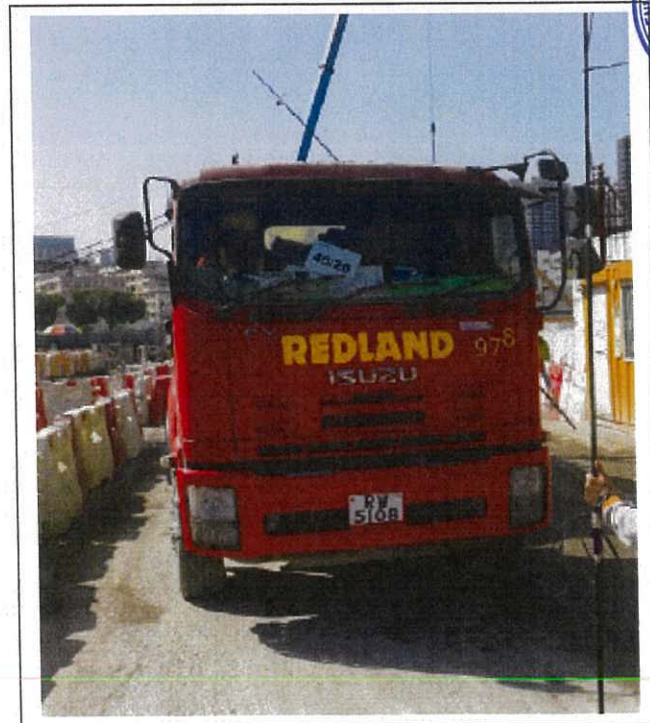


Concrete lorry mixer (Vehicle No. RW5108)
混凝土攪拌車 (車牌號碼 RW5108)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. TT3231)
混凝土攪拌車 (車牌號碼 TT3231)

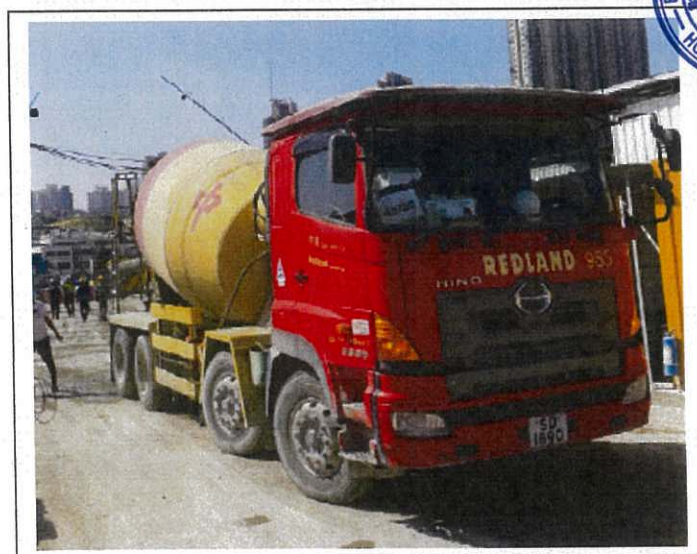

Concrete lorry mixer (Vehicle No. SD1890)
混凝土攪拌車 (車牌號碼 SD1890)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete lorry mixer (Vehicle No. TW5863)
混凝土攪拌車 (車牌號碼 TW5863)




Concrete lorry mixer (Vehicle No. TG5625)
混凝土攪拌車 (車牌號碼 TG5625)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Concrete pump, lorry mounted (Model No. 56X-6RZ / Serial No. ZLJ5430THBK)
混凝土泵，裝在貨車上 (型號 56X-6RZ / 序號 ZLJ5430THBK)

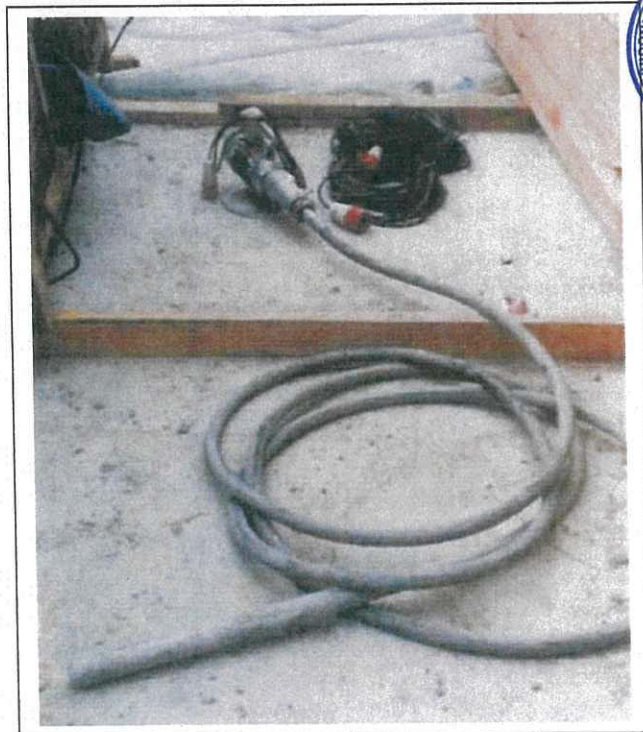

Poker, vibratory, hand-held (electric)
混凝土震動機，手提型 (電動)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Cherry picker
升降台



Scissor lifting platform
鉸剪式升降台



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



CNP 066 Dumper
卸土機




Forklift
鏟車



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片




CNP 122 Hoist, passenger/material (electric)
吊機，乘客/物料 (電動)

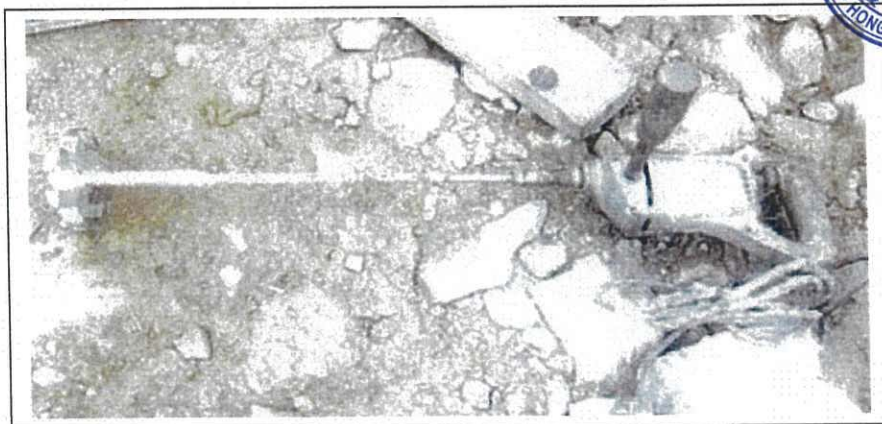


Mixer, hand-held (electric)
攪拌機，手提型 (電動)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片

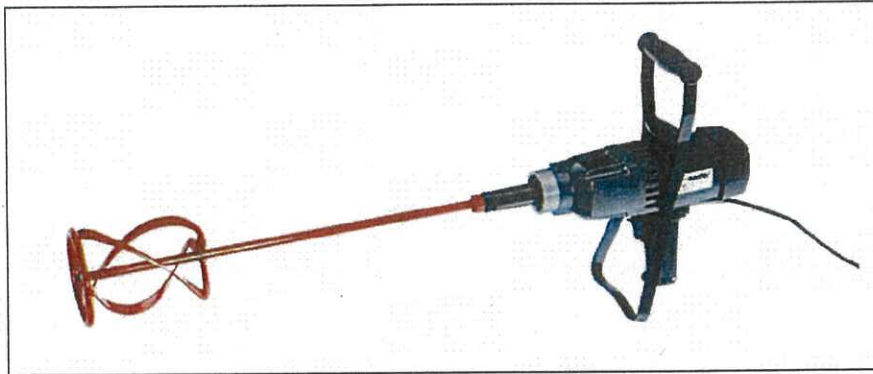

Agitator (electric)
攪動機 (電動)

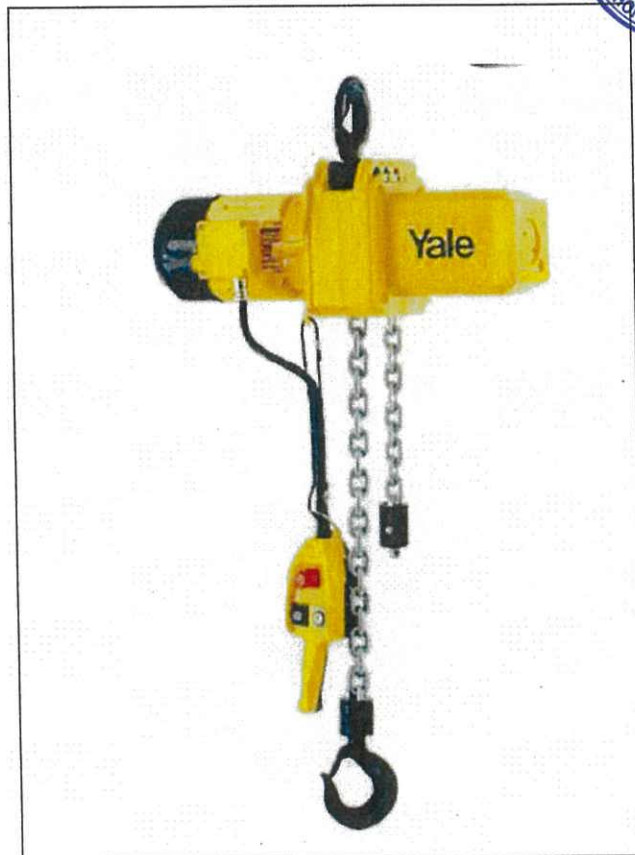

Chain hoist (electric)
鏈型吊機 (電動)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Gondola (electric)
吊船 (電動)



Needle scaler (pneumatic)
針束除銹機 (氣動)



Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Pallet truck (electric)
托盤車 (電動)




Crane, mobile (diesel), with Quality Powered Mechanical Equipment Label
showing a Sound Power Level ≤ 102 dB(A)

起重機，流動 (油渣)，備有優質機動設備標籤顯示聲功率級 ≤ 102 分貝(A)

Photograph(s) attached to Construction Noise Permit No. GW-RE1157-22
建築噪音許可證編號 GW-RE1157-22 的照片



Wrench, torque (electric)
扭力板手 (電動)

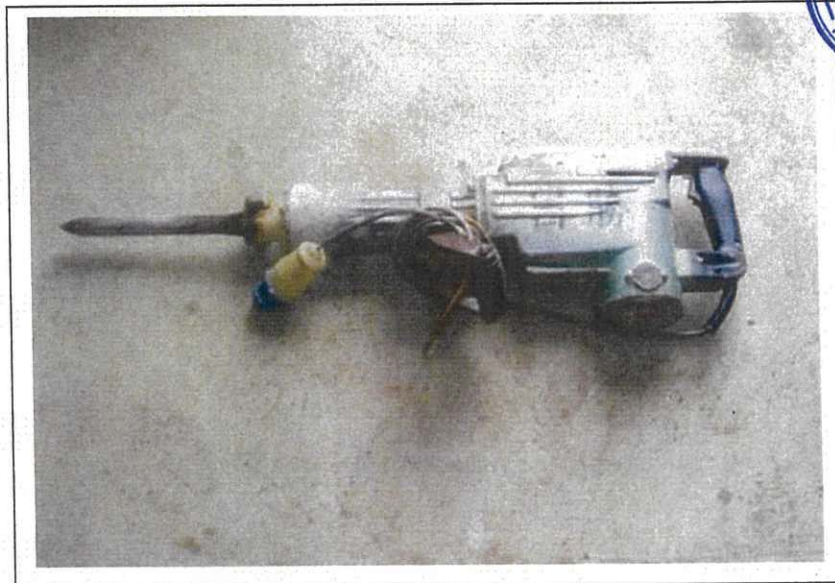


Breaker, hand-held (electric), with Noise Emission Label showing a
Sound Power Level ≤ 105 dB(A)
破碎機, 手提型 (電動), 備有噪音標籤顯示聲功率級 ≤ 105 分貝(A)



Location of Construction Site
建築地盤的位置

Location	Northing	Easting
A	820267	838165
B	820110	838329
C	820156	838372
D	820124	838405
E	820388	838601
F	820593	838570
G	820492	838235
H	820474	838257
I	820426	838246
J	820351	838246

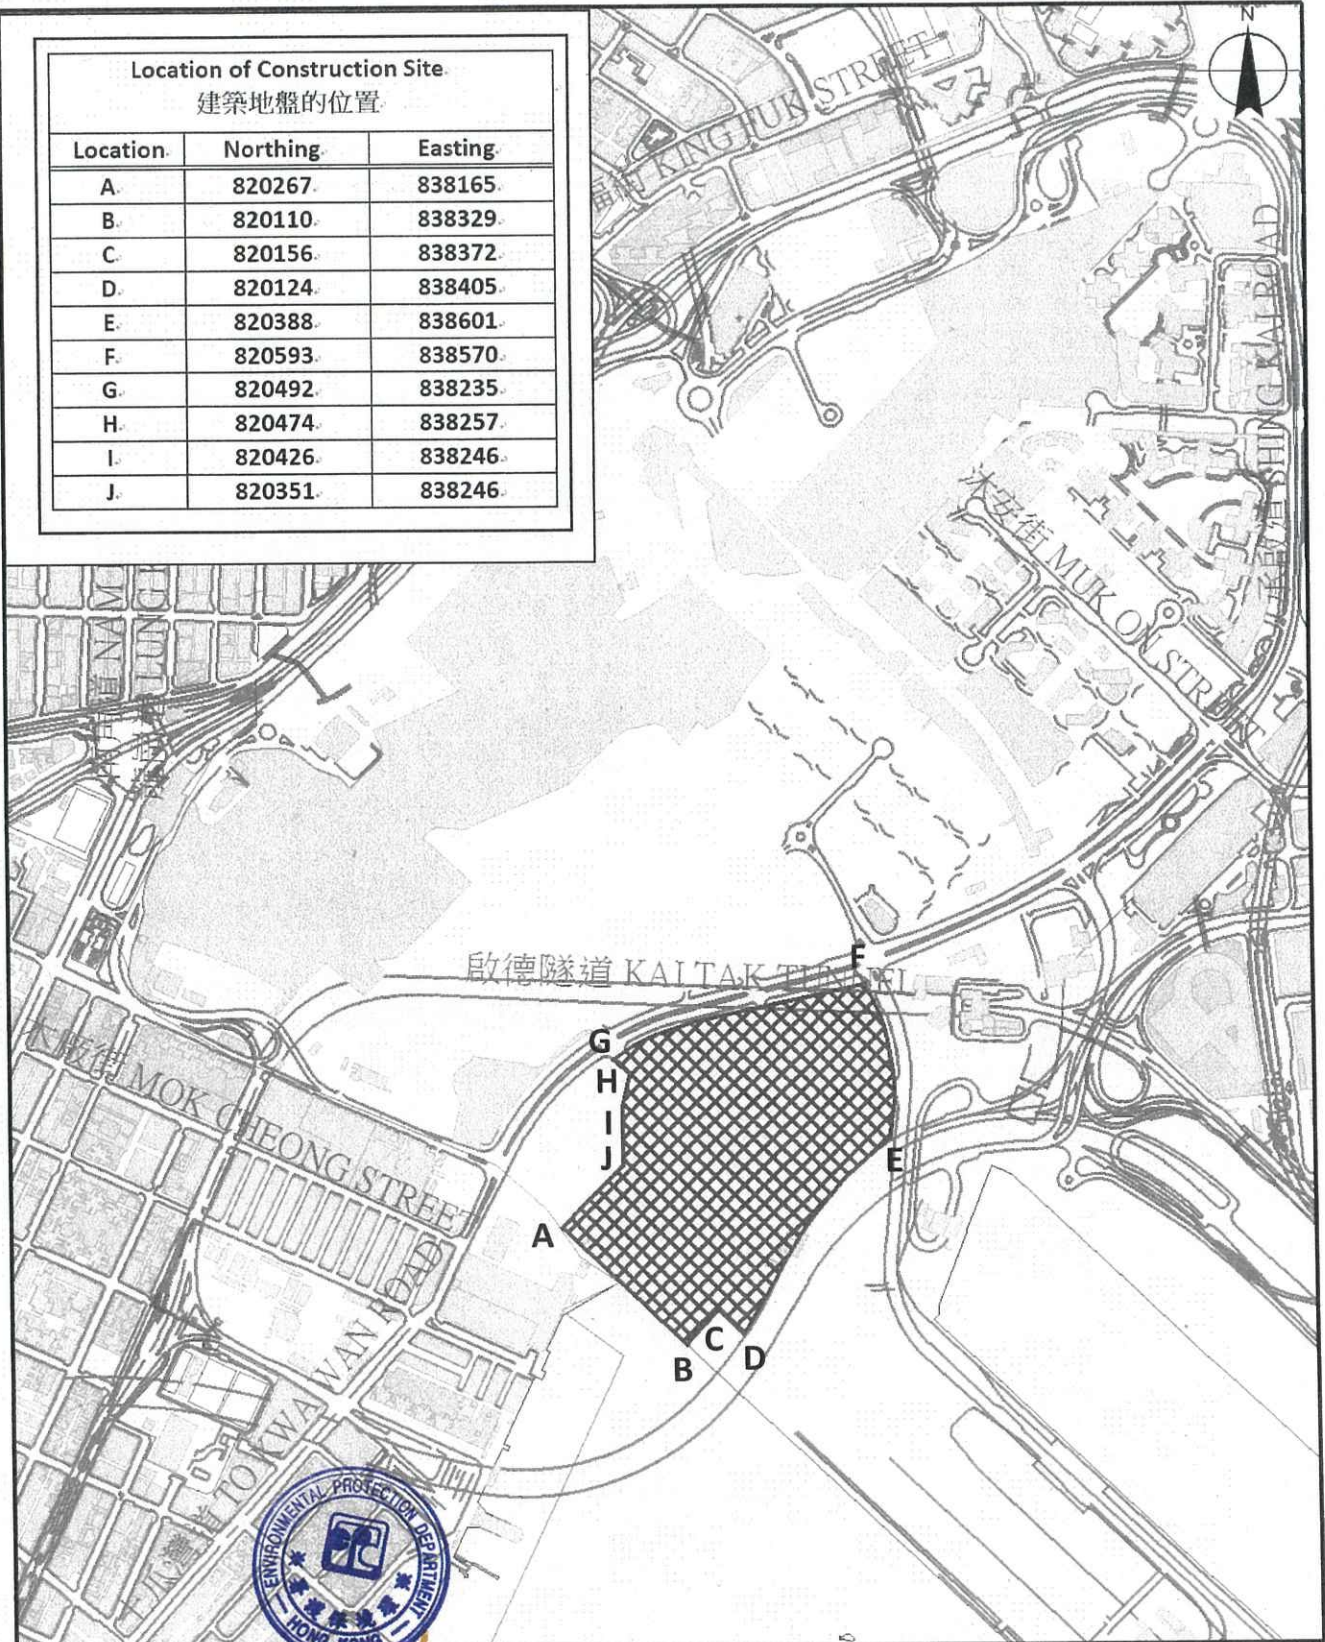

環境保護署

噪音管制監督

Environmental Protection Department Noise Control Authority

建築噪音許可證編號GW-RE1157-22的附圖

Plan attached to Construction Noise Permit No. GW-RE1157-22

圖例 Legend



建築地盤 Construction Site

比例 Scale 1:10,000

0 55 110 220 330 米Meters

Photo Records:



Photo 1: Photo of regular site inspection on 12 April 2023. (site area close to the Grand Waterfront)

Environmental Measure Implemented:



Photo 2: Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents



Photo 3: All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation.



協興工程有限公司
HIPHING ENGINEERING CO LTD

新創建集團成員 Member of NWS Holdings

備忘錄

致：各分判商 日期：22/3/2023
由：鍾展煒 工程編號：KT201901
地盤：啟德體育園項目 檔案編號：S22296/KT201901-Y03/CWC/SY

有關南區工地機動設備許可時間事宜

鑑於環境保護署近日多次於許可工作時間以外，即早上 7 點前及晚上 11 點後，巡視各啟德區工地，包括啟德體育園範圍，以確保工地有遵守建築噪音許可證之要求。環境保護署表示已發現本區有其他工地因違反相關要求而即時制止工地作業及，或會對該工地有進一步檢控行動。環境保護署表示因啟德區多個民居陸續入伙，環境保護署需加強巡視各工地以確保沒有建築噪音影響附近民居。環保署於日常巡查時亦重點提醒我司，必須**嚴格遵守**有關建築噪音許可證之要求，尤其注意必須遵守機動設備之組合以及許可建築工程所包括之範圍。


現跟據《噪音管制條例》，特意來函貴司，提醒以下事項：

1. 除持有指定時間車輛行駛許可證之車輛外，所有工地設備或車輛均不能於早上 7 點前或晚上 11 點後進入工地範圍工作。
2. 按建築噪音許可證之要求，於晚上 11 點後至隔天早上 7 點期間，工地只可使用水泵及發電機以緊急泵水之用，不得使用其他機動設備以進行建築工程。
3. 如有需要於晚上 7 點至晚上 11 點期間工作，請於晚上 10 點 45 分起停止工作並關上所有機動設備，以免因工作超時而引致投訴甚至檢控。

Photo 4: Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement.

Complaint Investigation Report

RECEIPT OF COMPLAINT		Ref: COM_0028
Date:	23 May 2023	
Time:	15:32	
From:	public complaint referred by EPD (EPD Ref.: K19/RE/00012659-23)	
Via:	email by contractor representative	
Contact no.:	-	
COMPLAINANT		
Name:	-	Address: -
Contact no.:	-	
DETAILS OF COMPLAINT		
Date:	19 May 2023	
Time:	-	
Parameter:*	Dust Noise Water Other (specify):	
Description:	<ul style="list-style-type: none"> - Complaint of discharging polluting wastewater from North Gate No. 4 at Muk Tai Street. - Please ensure the wastewater generated from your site to be properly treated and the discharge fulfill the conditions stipulated in the valid WPCO licence. - Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit. - Please take necessary measures to minimize the environmental nuisance arising from the construction site. 	
INVESTIGATION RESULT & RESPONSE		
ET, IEC and SOR notified on:	23 May 2023	
Investigation conducted on:	24 May 2023	
Result of investigation:	<p>Complaint investigation was carried out with contractor on 24 May 2023, the results of investigation were summarized as following:</p> <p>No discharge of polluting wastewater from North Gate No. 4 at Muk Tai Street was observed. (Photos 1a and 1b). The wastewater treatment plant on site was in normal condition. (Photos 2a, 2b and 2c) All wastewater effluent has been treated in accordance with the approved WPCO license (WT00034082-2019). (Photos 5a and 5b) All construction works carried out at northern site have been strictly followed the Construction Noise Permit requirement (GW-RE0400-23). (Photos 6a and 6b)</p> <p>In conclusion, water pollution control mitigation measures at the Kai Tak Sports Park have been implemented and maintained. All construction works carried out have been fulfilling the relevant environmental legislations, WPCO licence and CNP requirement during the concerned period.</p>	

RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS			
Environmental mitigation measures have been maintained as follow:			
1. Self-monitoring of wastewater discharge sample had been conducted and reported monthly. (Photo 3)			
2. Regular pest control measures had been provided near North Gate No. 4 Area. (Photo 4)			
Prepared by:	Sunny Chan	Title:	Environmental Team Leader
Signature:		Date:	25 May 2023

Attachment:
1. Photo Records

Photo Records:



Photo 1a and 1b: No discharge of polluting wastewater from North Gate No. 4 at Muk Tai Street was observed (24 May 2023).



Photo 2a, 2b and 2c: Wastewater treatment plant is set up at North 4 Gate and wastewater has been treated in accordance with the approved WPCO discharge license. (24 May 2023)

Environmental Measure Implemented:

Analytical Results

Sub-Matrix: WATER

Sample ID

WWTP Sample 7
(North 4)

Sampling date / time



03-Apr-2023

Compound	CAS Number	LOR	Unit	HK2312067-007
EA/ED: Physical and Aggregate Properties				
EA002: pH Value	----	0.1	pH Unit	7.8
EA025: Suspended Solids (SS)	----	2	mg/L	<2
EP: Aggregate Organics				
EP026C: Chemical Oxygen Demand	----	5	mg/L	9

Photo 3: Self-monitoring of wastewater discharge sample had been conducted and reported monthly.



Photo 4: Regular pest control measures had been provided near North Gate No. 4 Area.

Appendix 附錄

Licence No.: WT00034082-2019
牌照編號: WT00034082-2019

This Licence is Valid to: 30/06/2024
本牌照有效期至: 二零二四年六月三十日

ENVIRONMENTAL PROTECTION DEPARTMENT
環境保護署


WATER POLLUTION CONTROL ORDINANCE (CAP. 358)
水污染管制條例(第358章)

LICENCE PURSUANT TO SECTION 15/20/23A*
按第15 / 20/ 23A*條簽發的牌照

The Director of Environmental Protection (“the Authority”) grants this licence under the Water Pollution Control Ordinance (“the Ordinance”) on the terms and conditions stated below.

環境保護署署長(「監督」)按下列的條款及條件, 根據水污染管制條例(「本條例」)批給此牌照。

21 May 2020
Date
日期



(CHAN Wai-lun)
For the Authority
監督 (陳偉麟 代行)


PART A 甲部 : GENERAL TERMS 一般條款

Name of Licensee (“the Licensee”) 持牌人名稱(「持牌人」)	Hip Hing Engineering Company Limited 協興工程有限公司	
Discharge Premises (“the premises”) 排放處所(「處所」)	Construction Site of the Kai Tak Sports Park at Kai Tak, Kowloon City, Kowloon (HAB Contract No. HAB/KTSP/01) (See Annex I) 九龍九龍城啟德啟德體育園之建築地盤 (民政事務局合約編號: HAB/KTSP/01) (參見附件 I)	
Water Control Zone 水質管制區	Victoria Harbour (Phase Two) Water Control Zone 維多利亞港(第二期)水質管制區	
Discharge Category 排放種類	Discharge of industrial trade effluent 工業污水排放	
Nature of Discharge and Wastewater Treatment Facilities 排放性質及廢水處理設施	Effluent, Surface Run-off and all other wastewater discharges from the premises 上址排放的污水、地面徑流水及其他的廢水 Chemical precipitation, pH adjustment and Sedimentation tank 化學沉降、酸鹼值調節及沉澱池	
Discharge Point(s) 排放點	Stream A 水流 A: Discharge into communal storm water drain 排放入公用雨水渠	Stream B 水流 B: Discharge into inshore waters of Victoria Harbour 排放入維多利亞港沿岸水域
Sampling Point(s) 取樣點	Discharge outlet(s) of Wastewater Treatment Facility marked S.P.1 – S.P.8 on Annex II-IX 參見附件 II - IX 中標指 S.P.1 – S.P.8 的廢水處理設施的出水口	Discharge outlet(s) of Wastewater Treatment Facility marked S.P. 9 on Annex X 參見附件 X 中標指 S.P. 9 的廢水處理設施的出水口

*Delete as appropriate
將不適用者刪去

Reference No. 參考編號: EP682/286/0130/1

- 1 -

 Printed on Recycled Paper

EPD156

PART B 乙部 : SPECIFIC CONDITIONS 特別條件

B1. Limitations on Discharge 排放限制

The quantity and composition of any discharge from the premises shall not exceed the limits stated in the table below^(Note 4). All figures are upper limits unless otherwise indicated. All units are expressed as concentration in milligramme per litre unless otherwise stated.

任何源自處所之排放的量和成份不得超過下表所列的限度^(註4)。除另予表明外，所有數字均為上限。除另予說明外，所有單位均以毫克/升的濃度表示。

Determinand 測量物	Limit 限度	
	Stream A 水道 A	Stream B 水道 B
Flow Rate(m ³ / day) 流量(立方米/日)	3600	800
pH (pH units) 酸鹼值 (pH 單位)	6-9 [#]	6-9 [#]
Suspended Solids 懸浮固體	30	30
Chemical Oxygen Demand 化學需氧量	80	80

Range 上下限

B2. Self-monitoring and Reporting 自行監測及報告

- The Licensee shall perform self-monitoring as and when required by the Authority.
持牌人須在監督要求時進行自行監測。
- The Licensee shall sample the discharge at the Sampling Point(s) and, at his own expense carry out analyses in accordance with the sample type and measurement frequency specified for each determinand named below:-
持牌人須在取樣點為排放抽取樣本，並依照下列指定的測量物、取樣形式及頻率，自資予以分析。

Determinand 測量物	Unit 單位	Sample Type 取樣形式	Frequency 頻率
Suspended Solids 懸浮固體	mg/L 毫克/升	Grab 隨意取集	Monthly 每一個月一次

Results of these monitoring shall be summarized in a report on a Monthly/Bi-monthly/Quarterly/Yearly* basis and shall be submitted to the Authority.
所有監測結果須以摘要形式，每一個月/兩個月/三個月/年*作出報告，並須呈交監督審閱

*Delete as appropriate
將不適用者刪去

Photo 5a and 5b: Record of WPCO discharge licence - WT00034082-2019 .

FORM 3
NOISE CONTROL ORDINANCE
(Chapter 400)
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE0400-23

To : HIP HING ENGINEERING COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed :

Full address : Construction site of Kai Tak Sports Park (North), Kai Tak, Kowloon.

Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. * PART/WHOLE of the site falls * WITHIN/OUTSIDE a designated area.

3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
	Refer to attached sheet	

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 30 April 2023 at 0000 hours


Days and hours : 0000-2400 hours on general holiday (including Sunday), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday [but note condition 3.d.1. below for the operating hours within which the use of the above listed powered mechanical equipment is allowed].

This part of the permit expires on : 29 July 2023 at 2400 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.

- d. Other conditions imposed on the use of the powered mechanical equipment:

Refer to attached sheet.

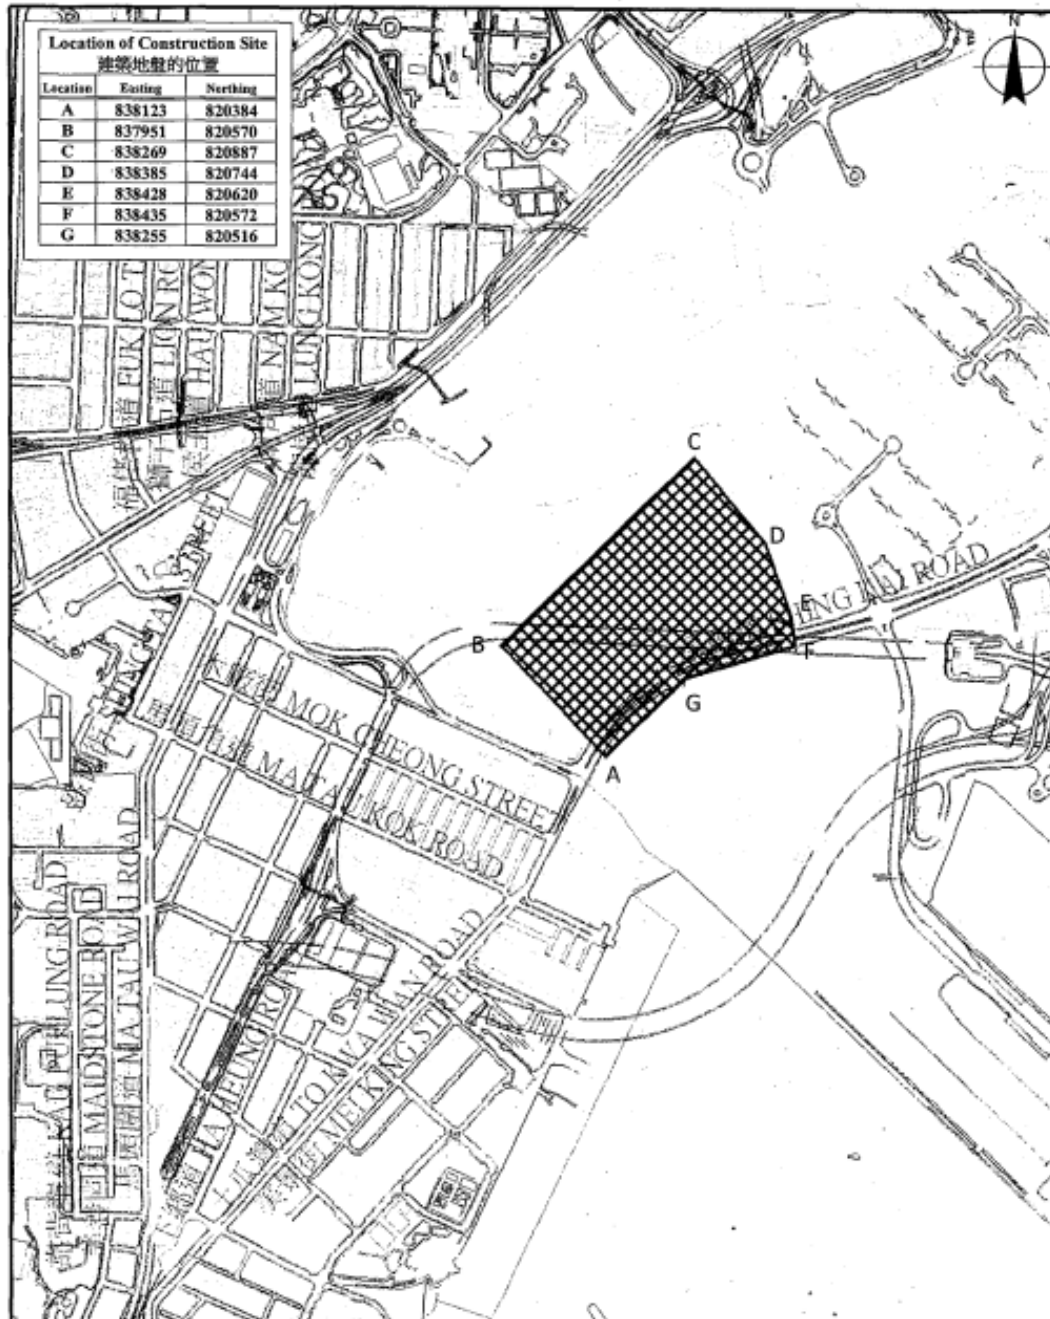

Location of Construction Site 建築地盤的位置		
Location	Easting	Northing
A	838123	820384
B	837951	820570
C	838269	820887
D	838385	820744
E	838428	820620
F	838435	820572
G	838255	820516

環境保護署

噪音管制監督

圖例 Legend

Environmental Protection Department Noise Control Authority

 建築地盤 Construction Site

建築噪音許可證編號 GW-RE0400-23 的附圖

比例 Scale 1:10,000

Plan attached to Construction Noise Permit No. GW-RE0400-23


 米 Meters
0 55 110 220 330

Photo 6a and 6b: Record of Construction Noise Permit - GW-RE0400-23.

Complaint Investigation Report

RECEIPT OF COMPLAINT		Ref: COM_0029
Date:	5 June 2023	
Time:	10:16	
From:	public complaint referred by EPD (EPD Ref.: K19/RE/00013539-23)	
Via:	email by contractor representative	
Contact no.:	-	
COMPLAINANT		
Name:	-	Address: -
Contact no.:	-	
DETAILS OF COMPLAINT		
Date:	31 May 2023	
Time:	-	
Parameter:*	Dust Noise Water Other (specify):	
Description:	<p>- Complaint of construction noise (piling work) from construction sites near Sung Wong Toi Road starting around 08:00am on weekdays</p> <p>- Please take necessary environmental measures to minimize the environmental nuisance arising from the construction site.</p>	
INVESTIGATION RESULT & RESPONSE		
ET, IEC and SOR notified on:	5 June 2023	
Investigation conducted on:	5 June 2023	
Result of investigation:	<p>Complaint investigation was carried out with contractor on 5 June 2023, the results of investigation were summarized as following:</p> <p>According to the contractor information, no piling work were scheduled at 08:00am along Sung Wong Toi Road during the complaint period. All construction works carried out on site have been strictly followed the Construction Noise Permit requirement. The CNP for the construction works at northern site (site area closest to the Sung Wong Toi Road) is attached for information. (Photos 5a and 5b)</p> <p>ET and contractor carried out regular site inspections at Kai Tak Sports Park on 23 May 2023. (Photo 1) Noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule were generally implemented during the time of inspection.</p> <p>According to the contractor information, noise mitigation control measures maintained on site included:</p> <p>1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents (Photo 2).</p> <p>In conclusion, noise control mitigation measures at the Kai Tak Sports Park have been implemented and maintained. All construction works carried out have been fulfilling the relevant environmental legislations and CNP requirement during the concerned period.</p>	

RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS

Environmental mitigation measures have been maintained as follow:

1. Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents (Photo 2)
2. All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation. (Photo 3)
3. Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement. (Photo 4)
4. Implementation of noise mitigation measures recommended in EIA's Environmental Mitigation Implementation Schedule.

Prepared by: Sunny Chan Title: Environmental Team Leader

Signature:  Date: 7 June 2023

Attachment:

1. Photo Records

Photo Records:



Photo 1: Photo of regular site inspection on 23 May 2023. (site area close to the Sung Wong Toi Road)

Environmental Measure Implemented:



Photo 2: Power Mechanical Equipment with Quality Power Mechanical Equipment (QPME) labels were used at site to lower the noise nuisance to the nearby residents .



Photo 3: All subcontractors are reminded to observe the latest Construction Noise Permit Requirement and the latest Construction Noise Permit had been provided to subcontractor for their observation.



備忘錄

致：各分判商 日期：02/05/2023

由：鍾偉克 工程編號：KT201901

地盤：啟德體育園項目 檔案編號：S23404/KT201901-Y03/WKC/SYY

有關北區建築噪音許可證更新事宜

環境保護署已於 2023 年 04 月 06 日更新北區建築噪音許可證，並於 2023 年 04 月 30 日晚 7 時正起生效，有效至 2023 年 07 月 29 日晚 12 時正。現特意提醒 貴司必須嚴格遵守有關要求，尤其注意必須遵守機動設備之組合以及許可建築工程所包括之範圍。

為確保 貴司遵守相關要求，如 貴司需於假日工作，請於星期三或前向 我司工地總管提交假日工作許可證，於假日工作許可證需填寫施工日期、公司名稱、當天工作之員工姓名及職位、負責人姓名及電話、施工位置及工作、施工時使用之機械及其數量。在遞交申請表後，需前往環保部參加噪音許可證專題訓練，且簽署表示遵守許可證內條款。我司工地總管、環保部及管理層會檢查當日施工活動有否抵觸建築噪音許可證內的條款及按工地實際需要作出審批，而已審批假日工作許可證會存放於工地出入口更亭內，於施工當日只容許已獲批分判商員工進入工地，未獲批准之員工將禁止進入工地。

請 貴司務必提醒所有工地人員切實遵守《噪音管制條例》，並確保進行的工序、所使用機動設備類形、數量及其使用位置符合建築噪音許可證內的條款。根據分判合約附錄《分判商對環境保護的責任》，在分判合約有效期間，政府所修定之新法例及分判合約所遺漏並已實行之法例，分判商亦須一律遵守。如有違反相關條例而導致總承建商遭受檢控或導致任何損失，一切費用及罰款將由分判商承擔。

協興工程有限公司

鍾偉克
助理合約經理

附件：北區建築噪音許可證 (GW-RE0400-23)

副本抄送：工程項目經理/ 工地總管/ 環保部/ 工料測量部

WKC/SYY/CHK/wms

Photo 4: Notice was provided to all subcontractors to follow the latest Construction Noise Permit Requirement.

FORM 3
NOISE CONTROL ORDINANCE
(Chapter 400)
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE0400-23

To: HIP HING ENGINEERING COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed :

Full address : Construction site of Kai Tak Sports Park (North), Kai Tak, Kowloon.

Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. * PART/WHOLE of the site falls * WITHIN/OUTSIDE a designated area.
3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
	Refer to attached sheet	

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 30 April 2023 at 0000 hours

Days and hours : 0000-2400 hours on general holiday (including Sunday), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday [but note condition 3.d.1. below for the operating hours within which the use of the above listed powered mechanical equipment is allowed].

This part of the permit expires on : 29 July 2023 at 2400 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.
d. Other conditions imposed on the use of the powered mechanical equipment:
Refer to attached sheet.

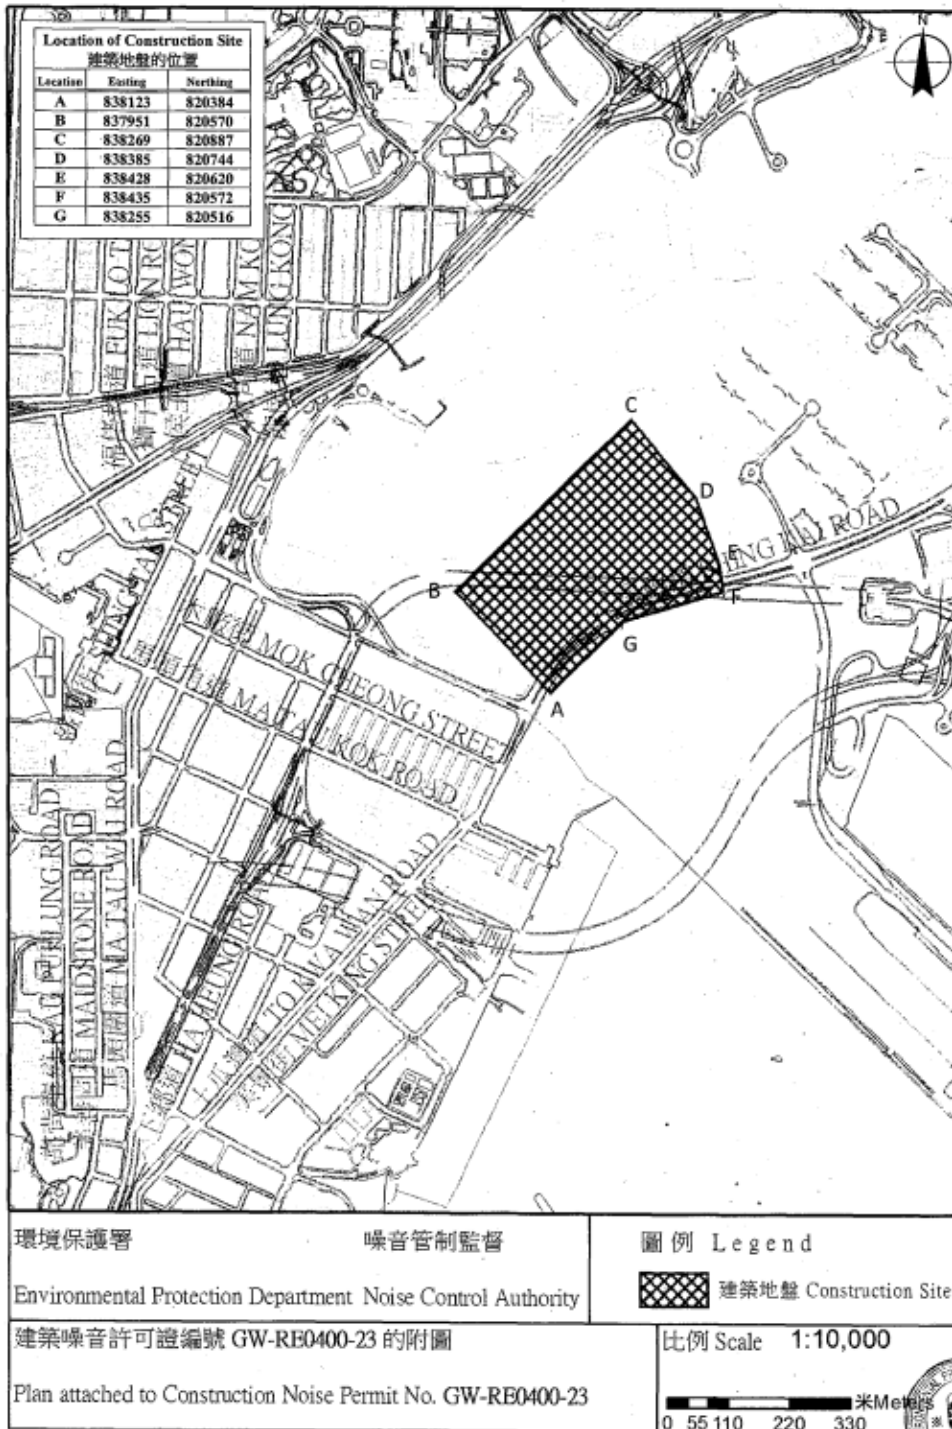


Photo 5a and 5b: Record of Construction Noise Permit - GW-RE0400-23.
