


# **Dragages-Nishimatsu Joint Venture**

**Contract No. DC/2007/10**  
**Design and Construction of Hong Kong**  
**West Drainage Tunnel**

Monthly EM&A Report  
(version 1.0)

October 2008

Approved By   
(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

**CINOTECH CONSULTANTS LTD**  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong  
Tel: (852) 2151 2083 Fax: (852) 3107 1388  
Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)

# TABLE OF CONTENTS

<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
Introduction .....	1
Environmental Monitoring Works.....	1
Environmental Licenses and Permits.....	3
Key Information in the Reporting Month.....	3
<b>1. INTRODUCTION.....</b>	<b>5</b>
Background.....	5
Project Organizations .....	5
Construction Programme .....	6
Summary of EM&A Requirements .....	7
<b>2. AIR QUALITY.....</b>	<b>9</b>
Monitoring Requirements.....	9
Monitoring Locations .....	9
Monitoring Equipment .....	9
Monitoring Parameters, Frequency and Duration .....	9
Monitoring Methodology and QA/QC Procedure .....	10
Results and Observations.....	12
<b>3. NOISE .....</b>	<b>14</b>
Monitoring Requirements.....	14
Monitoring Locations .....	14
Monitoring Equipment .....	14
Monitoring Parameters, Frequency and Duration .....	14
Monitoring Methodology and QA/QC Procedures .....	15
Maintenance and Calibration.....	15
Results and Observations.....	16
<b>4. WATER QUALITY.....</b>	<b>19</b>
Monitoring Requirements.....	19
Monitoring Locations .....	19
Monitoring Equipment .....	19
Monitoring Parameters, Frequency and Duration .....	20
Monitoring Methodology, Calibration Details and QA/QC Procedures .....	20
Results and Observations.....	21
Underground water level .....	21
<b>5. ENVIRONMENTAL AUDIT.....</b>	<b>23</b>
Site Audits .....	23
Review of Environmental Monitoring Procedures .....	23
Status of Environmental Licensing and Permitting .....	23
Status of Waste Management .....	23
Implementation Status of Environmental Mitigation Measures .....	24
Non-compliance Recorded during Site Inspections .....	27
Summary of Mitigation Measures Implemented .....	27
Implementation Status of Event Action Plans .....	28
Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution.....	28
<b>6. FUTURE KEY ISSUES.....</b>	<b>30</b>

Key Issues for the Coming Month.....	30
Monitoring Schedule for the Next Month .....	31
Construction Program for the Next Month.....	31
<b>7. CONCLUSIONS AND RECOMMENDATIONS .....</b>	<b>32</b>
Conclusions .....	32
Recommendations.....	32

## LIST OF TABLES

Table I	Summary Table for Non-compliance Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 1.2	Construction programme showing the inter-relationship with environmental protection/mitigation measures
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 2.4	Summary Table of Air Quality Monitoring Results during the reporting month
Table 3.1	Noise Monitoring Stations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Baseline Noise Level and Noise Limit Level for Monitoring Stations
Table 3.5	Summary Table of Noise Monitoring Results during the reporting month.
Table 4.1	Locations for Water Quality Monitoring
Table 4.2	Water Quality Monitoring Equipment
Table 4.3	Frequency and Parameters of Water Quality Monitoring
Table 4.4	Ground Water Level Monitoring Data at Location ADH48
Table 5.1	Summary of Environmental Licensing and Permit Status
Table 5.2	Observations and Recommendations of Site Inspections

## LIST OF FIGURES

Figure 1.1	Layout Plan of the Project Site
Figure 2.1	ET's Organization Chart
Figure 3.1a	Locations of Air Quality and Construction Noise Monitoring Stations at Eastern Portal
Figure 3.1b	Locations of Air Quality and Construction Noise Monitoring Stations at Western Portal
Figure 4.1a-b	Locations of Water Quality Monitoring Stations
Figure 4.2	Location of Ground Water Level Monitoring Stations

## **LIST OF APPENDICES**

A	Action and Limit Levels for Air Quality and Noise
B	Copies of Calibration Certificates
C	Quality Control Reports for SS Laboratory Analysis
D	Environmental Monitoring Schedules
E	1-hour TSP Monitoring Results, Graphical Presentations
F	24-hour TSP Monitoring Results, Graphical Presentations
G	Noise Monitoring Results and Graphical Presentations
H	Water Quality Monitoring Results and Graphical Presentations
I	Summary of Exceedance
J	Wind Data
K	Site Audit Summary
L	Environmental Mitigation Implementation Schedule (EMIS)
M	Event Action Plans
N	Complaint Logs
O	Construction Programme
P	Waste Generated Quantity

## **ABBREVIATION AND ACRONYM**

AL Levels	Action and Limit Levels
CEDD	Civil Engineering & Development Department
E / ER	Engineer/Engineer's Representative
EIA	Environmental Impact Assessment
EM&A	Environmental Monitoring and Audit
EMIS	Environmental Mitigation Implementation Schedule
EP	Environmental Permit
EPD	Environmental Protection Department
ET	Environmental Team
HVS	High Volume Sampler
IEC	Independent Environmental Checker
RE	Resident Engineer
RH	Relative Humidity
TSP	Total Suspended Particulates
QA/QC	Quality Assurance / Quality Control
SLM	Sound Level Meter
WMP	Waste Management Plan

## EXECUTIVE SUMMARY

### Introduction

1. This is the 7<sup>th</sup> Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for the “Drainage Improvement in Northern Hong Kong Island – Hong Kong West Drainage Tunnel” (the Project). This report documents the findings of EM&A Works conducted in October 2008.
2. The site activities undertaken in the reporting month included:
  - Further establishment of project organization and staffing.
  - Initial tunnel excavation and installation of temporary facilities at Eastern Portal.
  - Installation of temporary facilities, slope works, shallow & deep excavation works, marine works and arch tunnel excavation at Western Portal.
  - Utilities trial pits and additional ground investigation works at 14 nos. Intakes.
  - Approved in Principle (AIP) & Detailed Design Approval (DDA) submissions for temporary works at both portals.
  - AIP & DDA submissions for temporary and permanent works for 25 nos. Intakes.
  - AIP & DDA submissions for Pre-cast Segmental Lining at Adit Junction.
  - Environmental impact monitoring.
  - TBM design and fabrication overseas.

### Environmental Monitoring Works

3. Environmental monitoring for the Project was performed in accordance with the updated EM&A Manual and the monitoring results were checked and reviewed. Site audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.

4. Summary of the non-compliance of the reporting month is tabulated in Table I.

**Table I Summary Table for Non-compliance Recorded in the Reporting Month**

Parameter	No. of Exceedance		No. of Exceedance Due to the Project		Action Taken
	Action Level	Limit Level	Action Level	Limit Level	
Eastern Portal					
1-hr TSP	0	0	0	0	N/A
24-hr TSP	0	0	0	0	N/A
Noise	0	0	0	0	N/A
Western Portal					
1-hr TSP	0	0	0	0	N/A
24-hr TSP	0	0	0	0	N/A
Noise	0	0	0	0	N/A
Water	0	0	0	0	N/A

Eastern Portal

*1-hour TSP Monitoring*

5. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

*24-hour TSP Monitoring*

6. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

*Construction Noise*

7. All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Western Portal

*1-hour TSP Monitoring*

8. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

*24-hour TSP Monitoring*

9. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### *Construction Noise*

10. All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### *Water Quality*

11. All water quality monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

### **Environmental Licenses and Permits**

12. Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Project, An Environmental Permit No. EP-272/2007 was issued on 26 April 2007 and Environmental Permit No. EP-272/2007/A was issue on 26 October 2007. Later, the further Environmental Permit (FEP-01/272/2007/A) was issued on 28 January 2008 to Dragages-Nishimatsu Joint Venture as the Permit Holder.
13. Registration of Chemical Waste Producer (License: 5213-148-D2393-02 for Eastern Portal and No. 5213-172-D2393-01 for Western Portal), Water Discharge License (License No.: EP860/W10/XY0175 for Area of Mount Butler Office, EP860/W10/XY0177 for Eastern Portal and EP820/W9/XT086 for Western Portal) and Construction Noise Permit (License No.: GW-RS0612-08 for Eastern Portal and GW-RS0611-08 for Western Portal)

### **Key Information in the Reporting Month**

14. Summary of key information in the reporting month is tabulated in Table II.

**Table II Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Report (September 08)	Submitted to EPD on 16 October 2008 (EP condition 3.3)	Verified by IEC	---
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---



Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
<p><b><u>Future Key Issues:</u></b>                      Major site activities for the coming month include:</p> <ul style="list-style-type: none"> <li>• Tunnel excavation works and intake shaft works at Eastern Portal.</li> <li>• Tower crane installation, shallow and deep excavation works and arch tunnel excavation works at Western Portal.</li> <li>• Utilities trial pits and additional ground investigation works at 12 nos. Intake sites.</li> </ul>					

## 1. INTRODUCTION

### Background

- 1.1 Drainage Improvement in Northern Hong Kong Island – Hong Kong West Drainage Tunnel is a Designated Project (hereafter referred to as “the Project”) under the Environmental Impact Assessment Ordinance (Cap. 449). A study of environmental impact assessment (EIA) was undertaken to consider the key issues of air quality, noise, water quality, ecological, construction waste, landscape and visual, land use, cultural impacts, and identify possible mitigation measures associated with the works. An EIA Report was approved by the Environmental Protection Department (EPD) on 7 April 2006.
- 1.2 The project comprises the construction of a drainage tunnel deep into the ground in Mid-levels of the Northern Hong Kong Island from Tai Hang to Pokfulam to intercept and convey the stormwater from the upper catchment directly to the sea near Cyberport. The Drainage tunnel alignment starts from the Eastern Portal near Haw Par Mansion in Tai Hang and ends at the Western Portal located to the north of Cyberport running underneath the Pok Fu Lam, Tai Tam, Aberdeen and Lung Fu Shan Country Parks. The underground main drainage tunnel is 6.25m-7.25m in diameter and about 11km long. Two portals and a series of connecting adits and drop shafts are also been constructed. The general layout of the Project is shown in **Figure 1.1**.
- 1.3 An Environmental Permit (EP) No. EP-272/2007 was issued on 26 April 2007 for Drainage Improvement in Northern Hong Kong Island – Hong Kong West Drainage Tunnel to Drainage Services Department as the Permit Holder. Later, the further Environmental Permit (FEP-01/272/2007/A) was issued on 28 January 2008 to Dragages-Nishimatsu Joint Venture as the Permit Holder.
- 1.4 Cinotech Consultants Limited was commissioned by the Dragages-Nishimatsu Joint Venture (the Contractor) to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. The Updated EM&A Manual was prepared by Cinotech to fulfill the requirements of the EP. The construction commencement of this Contract at Eastern portal was on 17th April 2008 and 2nd May 2008 at Western Portal (land-based). The marine construction works was commenced on 30 May 2008. This is the 7th monthly EM&A report summarizing the EM&A works for the Project in October 2008 at Eastern and Western Portals.

### Project Organizations

- 1.5 Different parties with different levels of involvement in the project organization include:
  - Project Proponent – Drainage Services Department (DSD).
  - The Supervising Officer or Supervising Officer's Representative (SO or SOR) – Ove Arup & Partners (ARUP).
  - Environmental Team (ET) – Cinotech Consultants Limited (CCL).
  - Independent Environmental Checker (IEC) – Allied Environmental Consultants Limited (AEC).
  - Contractor - Dragages-Nishimatsu Joint Venture (DNJV).

1.6 The responsibilities of respective parties are detailed in Sections 1.14 to 1.28 of the updated EM&A Manual of the Project.

1.7 The key contacts of the Project are shown in Table 1.1 and the organization chart of ET is shown in **Figure 2.1**.

**Table 1.1 Key Project Contacts**

Party	Role	Name	Position	Phone No.	Fax No.
DNJV	Permit Holder	Mr. ALTIER Daniel	Project Manager	2671 7333	2671 9300
		Mr. UETAKE H.	Deputy Project Manager		
ARUP	Supervising Officer	Mr. Ted Tang	CRE	6117 6639	2436 1012
		Mr. Jackson Wong	SRE	6117 6636	
		Mr. Alan Ng	RE	9668 8350	
		Mr. Bernard Cheng	RE	98614939	
Cinotech	Environmental Team	Dr. Priscilla Choy	ET Leader	2151 2089	3107 1388
		Mr. Alex Ngai	Project Coordinator	2151 2076	
		Ms. Ivy Tam	Audit Team Leader	2151 2095	
		Mr. Henry Leung	Monitoring Team Leader	2151 2087	
AEC	Independent Environmental Checker	Ms. Claudine Lee	Independent Environmental Checker	2815 7028	2815 5399
DNJV	Contractor	Mr. Ben Ho	Environmental Officer	2671 7333	2671 9300

### Construction Programme

1.8 The site activities undertaken in the reporting month included:

- Further establishment of project organization and staffing.
- Initial tunnel excavation and installation of temporary facilities at Eastern Portal.
- Installation of temporary facilities, slope works, shallow & deep excavation works, marine works and arch tunnel excavation at Western Portal.
- Utilities trial pits and additional ground investigation works at 14 nos. Intakes.
- Approved in Principle (AIP) & Detailed Design Approval (DDA) submissions for temporary works at both portals.
- AIP & DDA submissions for temporary and permanent works for 25 nos. Intakes.

- AIP & DDA submissions for Pre-cast Segmental Lining at Adit Junction.
- Environmental impact monitoring.
- TBM design and fabrication overseas.

**Table 1.2 Construction programme showing the inter-relationship with environmental protection/mitigation measures**

Construction Works	Major Environmental Impact	Control Measures
Further establishment of project organization and staffing	Nil	Nil
Boulder stabilization, initial tunnel excavation and installation of temporary facilities at Eastern Portal	Noise and dust impact	Provided water spraying during the excavation works Provided temporary noise barriers.
Installation of temporary facilities, slope works, shallow & deep excavation works, marine works and arch tunnel excavation at Western Portal	Noise, dust, water quality impact and waste generation	Provided water spraying during slope and excavation works Provided silt curtain during the marine works On-site waste sorting and implementation of trip ticket system
Utilities trial pits and additional ground investigation works at 14 nos. Intakes	Nil	Nil
Approved in Principle (AIP) & Detailed Design Approval (DDA) submissions for temporary works at both portals	Nil	Nil
AIP & DDA submissions for temporary and permanent works for 25 nos. Intakes	Nil	Nil
AIP & DDA submissions for Pre-cast Segmental Lining at Adit Junction		
Environmental impact monitoring	Nil	Nil
TBM design and fabrication overseas	Noise Impact and ground water	Double-shielded Tunnel Boring Machine to minimize seepage of groundwater

### Summary of EM&A Requirements

1.9 The EM&A programme requires construction phase monitoring construction noise, air quality and water quality and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:

- All monitoring parameters;
- Action and Limit levels for all environmental parameters;
- Event Action Plans;
- Environmental mitigation measures, as recommended in the project EIA study final report; and

- Environmental requirements in contract documents.
- 1.10 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 5 of this report.
- 1.11 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely air quality, water quality and noise levels and audit works for the Project in October 2008.

**2. AIR QUALITY**

**Monitoring Requirements**

2.1 1-hour and 24-hour TSP monitoring were conducted to monitor the air quality at Eastern and Western Portals. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

**Monitoring Locations**

2.2 Three designated monitoring stations, AQ1, AQ2 and AQ3 were selected for impact dust monitoring. Table 2.1 describes the air quality monitoring locations, which are also depicted in **Figure 3.1a-b**.

**Table 2.1 Locations for Air Quality Monitoring**

Monitoring Stations	Locations
AQ1	True Light Middle School of Hong Kong
AQ2	Outside Aegean Terrace
AQ3	Outside The Site Office at Western Portal

**Monitoring Equipment**

2.3 Table 2.2 summarizes the equipment used in the impact air monitoring programme. Copies of calibration certificates are attached in **Appendix B**.

**Table 2.2 Air Quality Monitoring Equipment**

Equipment	Model and Make	Quantity
Calibrator	G25A; S/N: 1536	1
1-hour TSP Dust Meter	Laser Dust Monitor – Model LD3	1
HVS Sampler	GMWS 2310 c/w of TSP sampling inlet	2

**Monitoring Parameters, Frequency and Duration**

2.4 Table 2.3 summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period. The air quality monitoring schedule for the reporting month is shown in **Appendix D**.

**Table 2.3 Impact Dust Monitoring Parameters, Frequency and Duration**

Parameters	Frequency
1-hr TSP	Three times / 6 days
24-hr TSP	Once / 6 days

## Monitoring Methodology and QA/QC Procedure

### *1-hour TSP Monitoring*

#### Measuring Procedures

2.5 The measuring procedures of the 1-hour dust meters were in accordance with the Manufacturer's Instruction Manual as follows:

- Pull up the air sampling inlet cover
- Change the Mode 0 to BG with once
- Push Start/Stop switch once
- Turn the knob to SENSI.ADJ and press it
- Push Start/Stop switch once
- Return the knob to the position MEASURE slowly
- Push the timer set switch to set measuring time
- Remove the cap and make a measurement

#### Maintenance/Calibration

2.6 The following maintenance/calibration was required for the direct dust meters:

- Check the meter at a 3-month interval and calibrate the meter at a 1-year interval throughout all stages of the air quality monitoring.

### *24-hour TSP Monitoring*

#### Instrumentation

2.7 High volume (HVS) samplers (Model GMWS-2310 Accu-Vol) completed with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50). Moreover, the HVS also met all the requirements in section 2.5 of the updated EM&A Manual.

#### Operating/Analytical Procedures

2.8 Operating/analytical procedures for the operation of HVS were as follows:

- A horizontal platform was provided with appropriate support to secure the samplers against gusty wind.
- No two samplers were placed less than 2 meters apart.
- The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2 meters of separation from walls, parapets and penthouses was required for rooftop samples.
- A minimum of 2 meters separation from any supporting structure, measured horizontally was required.
- No furnaces or incineration flues were nearby.
- Airflow around the sampler was unrestricted.

- The sampler was more than 20 meters from the drip line.
  - Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.
- 2.9 Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 1.1 m<sup>3</sup>/min. and 1.4 m<sup>3</sup>/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.
- 2.10 For TSP sampling, fiberglass filters (G810) were used [Note: these filters have a collection efficiency of > 99% for particles of 0.3 mm diameter].
- 2.11 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 2.12 The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
- 2.13 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- 2.14 The shelter lid was closed and secured with the aluminum strip.
- 2.15 The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- 2.16 After sampling, the filter was removed and sent to the HOKLAS laboratory (Wellab Ltd.) for weighing. The elapsed time was also recorded.
- 2.17 Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%.

#### Maintenance/Calibration

- 2.18 The following maintenance/calibration was required for the HVS:
- The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
  - High volume samplers were calibrated at bi-monthly intervals using GMW-25 Calibration Kit throughout all stages of the air quality monitoring.



## Results and Observations

### Eastern Portal (AQ1)

- 2.19 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 2.20 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

### Western Portal (AQ2)

- 2.21 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

### Western Portal (AQ3)

- 2.22 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 2.23 Wind data was obtained from the Meteorological Observations for King's Park Automatic Weather Station for Eastern Portal and Wong Chuk Hang Automatic Weather Station for Western Portal. These wind data for the reporting period is summarized in **Appendix J**.
- 2.24 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in **Appendices E and F** respectively.
- 2.25 In accordance with Condition 4.2 of the EP, all environmental monitoring data was made available to the public via internet access at the website <http://www.cinotech.com.hk/projects/WestDrainageTunnel/>.
- 2.26 According to our field observations, the identified dust sources at the monitoring stations were mainly from the excavation works and the road traffic for Eastern and Western Portals.

**Table 2.4 Summary Table of Air Quality Monitoring Results during the reporting month**

Parameter	Date	Concentration (µg/m <sup>3</sup> )	Action Level, µg/m <sup>3</sup>	Limit Level, µg/m <sup>3</sup>
<b>Eastern Portal</b>				
1-hr TSP (AQ1)	3-Oct-08	184.5	345	500
	6-Oct-08	286.0		
	9-Oct-08	82.9		
	10-Oct-08	77.6		
	14-Oct-08	206.6		
	15-Oct-08	159.8		
	16-Oct-08	223.0		
	21-Oct-08	328.1		
	22-Oct-08	105.8		
	23-Oct-08	223.0		
	28-Oct-08	154.2		
	29-Oct-08	238.0		
	31-Oct-08	232.4		
24-hr TSP (AQ1)	8-Oct-08	93.4	201	260
	9-Oct-08	65.0		
	15-Oct-08	100.0		
	21-Oct-08	89.4		
	27-Oct-08	136.4		
<b>Western Portal</b>				
1-hr TSP (AQ2)	3-Oct-08	32.9	321	500
	6-Oct-08	35.3		
	9-Oct-08	37.2		
	10-Oct-08	37.2		
	14-Oct-08	49.5		
	15-Oct-08	48.3		
	16-Oct-08	52.9		
	21-Oct-08	37.5		
	22-Oct-08	50.4		
	23-Oct-08	46.3		
	28-Oct-08	51.2		
	29-Oct-08	53.1		
	31-Oct-08	46.7		
24-hr TSP (AQ3)	3-Oct-08	87.4	156	260
	9-Oct-08	68.3		
	15-Oct-08	95.7		
	21-Oct-08	27.4		
	27-Oct-08	62.0		

### 3. NOISE

#### Monitoring Requirements

- 3.1 Three noise monitoring stations, namely NC1, NC2 and NC3 were selected for impact monitoring. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

#### Monitoring Locations

- 3.2 Noise monitoring was conducted at three designated monitoring stations as listed in Table 3.1. **Figure 3.1a-b** shows the locations of these stations.

**Table 3.1 Noise Monitoring Stations**

Monitoring Stations	Locations
NC1	True Light Middle School of Hong Kong
NC2	The Legend
NC3	Outside Aegean Terrace

#### Monitoring Equipment

- 3.3 Table 3.2 summarizes the noise monitoring equipment. Copies of calibration certificates are provided in **Appendix B**.

**Table 3.2 Noise Monitoring Equipment**

Equipment	Model and Make	Qty.
Integrating Sound Level Meter	B&K Model 2238 and SVAN 955	3
Calibrator	B&K 4231 and SV30A	3

#### Monitoring Parameters, Frequency and Duration

- 3.4 Table 3.3 summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix D**.

**Table 3.3 Noise Monitoring Parameters, Frequency and Duration**

Monitoring Stations	Parameter	Period	Frequency	Measurement
NC1 NC2 NC3	L <sub>10</sub> (30 min.) dB(A) L <sub>90</sub> (30 min.) dB(A) L <sub>eq</sub> (30 min.) dB(A)	0700-1900 hrs on normal weekdays	Once per week	Façade
NC2 NC3	L <sub>eq</sub> (5 min.) dB(A)	0700 - 2300 hrs holidays & 1900 - 2300 hrs on all other days		

**Monitoring Methodology and QA/QC Procedures**

- The Sound Level Meter was set on a tripod at a height of 1.2 m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels were adjusted with a correction of +3 dB(A).
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting : A
  - time weighting : Fast
  - time measurement : 30 minutes / 5 minutes
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the L<sub>eq</sub>, L<sub>90</sub> and L<sub>10</sub> were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Noise measurement was paused temporarily during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

**Maintenance and Calibration**

- 3.5 The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- 3.6 The sound level meter and calibrator were checked and calibrated at yearly intervals.
- 3.7 Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels

from before and after the noise measurement agree to within 1.0 dB.

### **Results and Observations**

- 3.8 Noise monitoring (0700-1900 on normal weekdays) at the three designated locations was conducted as scheduled in the reporting month. As the construction works at Western Portal were carried out at 1900-2300 on all other days and 0700-2300 on holidays since 19 October 2008 and at 1900-2300 on all other days since 27 October 2008 for Eastern Portal, noise monitoring at NC2 and NC3 were also conducted for the restricted hours. As the monitoring station at NC1 during the restricted hours was not confirmed in October 2008. No noise monitoring for the restricted hours at NC1 was conducted.

#### Eastern Portal (NC1 & NC2)

- 3.9 No Action/Limit Level exceedance was recorded.

#### Western Portal (NC3)

- 3.10 No Action/Limit Level exceedance was recorded.
- 3.11 All the Construction Noise Levels (CNLs) reported in this report were adjusted with the corresponding baseline level (i.e. Measured Leq – Baseline Leq = Measured CNL), in order to facilitate the interpretation of the noise exceedance. The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented at Table 3.4.
- 3.12 Noise monitoring results and graphical presentations are shown in **Appendix G**. In accordance with Condition 4.2 of the EP, all environmental monitoring data was made available to the public via internet access at the website <http://www.cinotech.com.hk/projects/WestDrainageTunnel/>.
- 3.13 The major noise source identified at the designated noise monitoring stations was the traffic noise along the Tai Hang Road, rock breaking and excavation works for Eastern Portal and pile piling for Western Portal.

**Table 3.4 Baseline Noise Level and Noise Limit Level for Monitoring Stations**

Station	Baseline Noise Level, dB (A)	Noise Limit Level, dB (A)
NC1 – True Light Middle School of Hong Kong	70.2 (at 0700 – 1900 hrs on normal weekdays)	70* (at 0700 – 1900 hrs on normal weekdays)
NC2 – The Legend	64.8 (at 0700 – 1900 hrs on normal weekdays) 59.5 (at 0700 - 2300 hrs holidays & 1900 - 2300 hrs on all other days )	75 (at 0700 – 1900 hrs on normal weekdays) 65 (at 0700 - 2300 hrs holidays & 1900 - 2300 hrs on all other days )
NC3 – Outside Aegean Terrace	57.7 (at 0700 – 1900 hrs on normal weekdays) 53.8 (at 0700 - 2300 hrs holidays & 1900 - 2300 hrs on all other days )	75 (at 0700 – 1900 hrs on normal weekdays) 65 (at 0700 - 2300 hrs holidays & 1900 - 2300 hrs on all other days )

(\*) reduce to 65 dB(A) during school examination periods.

**Table 3.5 Summary Table of Noise Monitoring Results during the reporting month**

Parameter	Date	Construction Noise Level : Leq(30min) dB (A)	Action Level	Limit Level,
Eastern Portal				
NC1	3-Oct-08	67.8, Measured $\leq$ Baseline	When one documented compliant is received	70*dB(A)
	9-Oct-08	67.8, Measured $\leq$ Baseline		
	14-Oct-08	64.2, Measured $\leq$ Baseline		
	23-Oct-08	68.7, Measured $\leq$ Baseline		
	31-Oct-08	68.2, Measured $\leq$ Baseline		
NC2	3-Oct-08	53.3		75dB(A)
	9-Oct-08	60.2		
	14-Oct-08	62.8, Measured $\leq$ Baseline		
	23-Oct-08	67.2		
	31-Oct-08	63.2		
Western Portal				
NC3	3-Oct-08	54.2	When one documented compliant is received	75dB(A)
	9-Oct-08	56.6		
	14-Oct-08	49.4		
	23-Oct-08	56.8		
	31-Oct-08	56.8		
<b>(Restricted Hours - 07:00 - 23:00 hrs holidays &amp; 19:00 - 23:00 hrs on all other days )</b>				
Parameter	Date	Construction Noise Level : Leq(5min) dB (A)	Action Level	Limit Level,
Eastern Portal				
NC2	31-Oct-08	59.5	When one documented compliant is received	65dB(A)
Western Portal				
NC3	19-Oct-08	58.6	When one documented compliant is received	65dB(A)
	23-Oct-08	50.6		
	26-Oct-08	58.0		
	31-Oct-08	50.4		

(\*) reduce to 65 dB(A) during school examination periods.

#### 4. WATER QUALITY

##### Monitoring Requirements

4.1 Dissolved oxygen (DO concentration in mg/L and DO saturation in percentage), Turbidity (Tby in NTU), Suspended Solid (SS in mg/L), pH, salinity and both water and ambient temperature monitoring were conducted to monitor the water quality. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

##### Monitoring Locations

4.2 Locations of designated Water Quality Monitoring Stations are shown in **Figure 4.1a-b** and described in Table 4.1. Samples shall be taken at all designated Monitoring and Control Stations.

**Table 4.1 Locations for Water Quality Monitoring**

Monitoring Stations	Coordinates	
	Northing	Easting
<b>Control Stations</b>		
CE (Ebb)	814956	830026
CF (Flood)	812420	831778
<b>Impact Stations</b>		
I1	813654	831088
I2	813582	831105
Intake A	813044	831603
Intake B	814583	830606

##### Monitoring Equipment

4.3 Table 4.2 summarizes the equipment used in the water quality monitoring program. All the monitoring equipment complied with the specifications stipulated in the Updated EM&A Manual. Copies of the calibration certificates of the equipment are shown in **Appendix B**.

**Table 4.2 Water Quality Monitoring Equipment**

Equipment	Model and Make	Qty.
Water Sampler	Kahlsico Water-Bottle Model 135DW 150	1
Multi-parameter Water Quality System	YSI 6820	2
Monitoring Position Equipment	“Magellan” Handheld GPS Model GPS-320	1



**Monitoring Parameters, Frequency and Duration**

4.4 Table 4.3 summarizes the monitoring parameters, monitoring period and frequencies of water quality monitoring.

**Table 4.3 Frequency and Parameters of Water Quality Monitoring**

Station	Parameters	Frequency	No. of depth sampled	Depth	No. of samples events
CE	<ul style="list-style-type: none"> <li>• Temperature (°C)</li> <li>• pH (pH unit)</li> <li>• turbidity (NTU)</li> <li>• water depth (m)</li> <li>• salinity (mg/L)</li> <li>• dissolved oxygen (DO) (mg/L and % of saturation)</li> <li>• suspended solids (SS) (mg/L)</li> </ul>	3 times per week during the course of the marine works	3	<ul style="list-style-type: none"> <li>• 3 water depths: 1m below water surface, mid-depth and 1m above sea bed.</li> <li>• If the water depth is less than 3m, mid-depth sampling only.</li> <li>• If the water depth is less than 6m, omit mid-depth sampling.</li> </ul>	2 per monitoring day (1 for mid-ebb and 1 for mid-flood)
CF			2		
I1			3		
I2			3		
Intake A			3		
Intake B			3		

**Monitoring Methodology, Calibration Details and QA/QC Procedures**

Instrumentation

4.5 A multi-parameter meter (Model YSI 6820 C-M) was used to measure DO, DO saturation, turbidity, salinity and temperature.

Operating/Analytical Procedures

4.6 At each measurement, two consecutive measurements of DO concentration, DO saturation, salinity, turbidity and temperature were taken. Where the difference in the value between the first and second readings of each set was more than 25% of the value of the first reading, the reading was discarded and further readings were taken.

4.7 For SS measurement, duplicate water samples for SS were taken and analysed at each monitoring station at each sample depth. The sample bottles were then packed in cool-

boxes (without being frozen), and delivered to a HOKLAS accredited laboratory for analysis of suspended solids concentrations within 24 hours.

#### Maintenance and Calibration

- 4.8 Before each round of monitoring, a zero check in distilled water was performed with the turbidity probe of YSI 6820-C-M. The probe was then calibrated with a solution of known NTU.
- 4.9 QA/QC procedures as attached in **Appendix C** are available for the SS analyzed in the HOKLAS-accredited laboratory, WELLAB Ltd.

#### **Results and Observations**

- 4.10 All water quality monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. The monitoring data and graphical presentations of the monitoring results are shown in **Appendix H**.
- 4.11 In accordance with Condition 4.2 of the EP, all environmental monitoring data was made available to the public via internet access at the website <http://www.cinotech.com.hk/projects/WestDrainageTunnel/>.
- 4.12 During the water quality monitoring, the areas of inspection included the general environmental conditions in the vicinity of the site, pollution control and mitigation measures within the site; and also review on the environmental conditions outside the site area that are likely to be affected, directly or indirectly, by site activities. The findings have been recorded in our Field Record Sheets.
- 4.13 No Action/Limit Level exceedance was recorded.
- 4.14 The summary of exceedance record in reporting month is shown in **Appendix I**.

#### **Underground water level**

- 4.15 Ground water levels were measured once per month during the construction phase in order to ensure the water levels at those intakes near to the natural stream courses and thus on the surrounding habitats will not be significantly affected.
- 4.16 Locations of designated ground water level (borehole with piezometer) monitoring station UC1 at Eastern Portal has been changed to ADH48 which was verified by IEC on 5th June 2008. Ground water level monitoring location is shown in **Figure 4.2** and the Monitoring data are shown in Table 4.4

**Table 4.4 Ground Water Level Monitoring Data at Location ADH48**

<b>Date</b>	<b>Water Level (from ground)/m</b>
16 October 2008	8.01
25 October 2008	8.10

## 5. ENVIRONMENTAL AUDIT

### Site Audits

- 5.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix K**.
- 5.2 Site audits were conducted on 10<sup>th</sup>, 15<sup>th</sup>, 22<sup>nd</sup> and 30<sup>th</sup> October 2008. IEC site inspections were conducted on 30<sup>th</sup> October 2008. No non-compliance was observed during the site audits.

### Review of Environmental Monitoring Procedures

- 5.3 The monitoring works conducted by the monitoring team were inspected regularly. The following observations have been recorded for the monitoring works:

#### *Air Quality Monitoring*

- The monitoring team recorded all observations around the monitoring stations within and outside the construction site.
- The monitoring team recorded the temperature and weather conditions on the monitoring days.

#### *Noise Monitoring*

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- Major noise sources were identified and recorded. Other intrusive noise attributing to the result was trimmed off by pausing the monitoring temporarily.

#### *Water Quality Monitoring*

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- The monitoring team recorded the weather condition on the monitoring day.

### Status of Environmental Licensing and Permitting

- 5.4 All permits/licenses obtained for the Project are summarized in Table 5.1.

### Status of Waste Management

- 5.5 The waste management of the Project has to follow the requirements and procedures stated in the Waste Management Plan which was prepared by the Contractor.

- 5.6 During this reporting period, a total 5 nos. of dump trucks of waste were delivered to SENT landfill and 498 nos. of C&D waste was delivered to Public Fill Reception Facilities. Both the trip ticket system and chit accounting system for disposal of waste were operating smoothly to date. No overloading case was recorded during this reporting period. No disposal of inert C&D material to public sorting facilities and no dump truck without cover were reported from CEDD. In respect of the dump truck cover, DNJV keeps on take record photos and inspection to ensure that all dump trucks have fully covered the skip before leaving the site.
- 5.7 The amount of wastes generated by the activities of the Project during the reporting month is shown in **Appendix P**.

**Table 5.1 Summary of Environmental Licensing and Permit Status**

Permit No.	Valid Period		Details	Status
	From	To		
<b>Environmental Permit (EP)</b>				
FEP-01/272/2007/A	28/1/08	N/A	Construction of a 6.25m-7.25m in diameter and about 11 km long underground main drainage tunnel, 2 portals and a series of connecting adits and drop shafts.	Valid
<b>Effluent Discharge License</b>				
EP860/W10/XY0175	23/06/08	30/06/13	Industrial discharge (Area of Mount Butler Office)	Valid
EP860/W10/XY0177	23/06/08	30/06/13	Industrial discharge (Eastern Portal Site)	Valid
EP820/W9/XT086	22/07/08	31/07/13	Industrial discharge (Western Portal Site)	Valid
<b>Registration of Chemical Waste Producer</b>				
5213-148-D2393-02	---	N/A	Chemical waste types: Spent oil	Valid
5213-172-D2393-01	---	N/A	Chemical waste types: Spent oil	Valid
<b>Construction Noise Permit (CNP)</b>				
GW-RS0612-08	07/09/08	06/03/09	Construction Noise Permit for the use of powered mechanical equipment for carrying out construction work at Hong Kong West Drainage Tunnel (Eastern Portal) (DSD Contract No. DC/2007/10), Tai Hang Road, Causeway Bay, Hong Kong.	Valid
GW-RS0611-08	01/09/08	28/02/09	Construction Noise Permit for the use of powered mechanical equipment for carrying out construction work at Cyberport Road near Cyberport Sewage Treatment Plant, Cyberport, Hong Kong.	Valid

### Implementation Status of Environmental Mitigation Measures

- 5.8 During site inspections in the reporting month, no non-conformance was identified. ET weekly site inspections were carried out during the reporting month and the observations and recommendations are summarized in Table 5.2.

**Table 5.2 Observations and Recommendations of Site Inspections**

<b>Parameters</b>	<b>Date</b>	<b>Observations and Recommendations</b>	<b>Follow-up</b>
<b><i>Water Quality</i></b>	10/10/2008	Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.	*Follow-up action was needed for the item.
	15/10/2008	Silty water was observed accumulate at the tank at Intake W3. The Contractor was reminded to clear them to prevent overflow during the rainstorm.	Rectification/improvement was observed during the follow-up audit session.
	15/10/2008	Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.	*Follow-up action was needed for the item.
	22/10/2008	Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.	The item was not observed during the follow-up audit session.
	30/10/2008	Leakage of water from the construction site at the bottom of hoarding at Eastern Portal was observed. The Contractor was reminded to seal the hoarding properly.	The item was not rectified during the follow-up audit session.
	30/10/2008	Stagnant water was observed at the pit area and drip tray at Eastern Portal. The Contractor was reminded to dry it out.	Rectification/improvement was observed during the follow-up audit session.
	30/10/2008	Drainage channel to nullah was observed accumulate with construction material at Western Portal. The Contractor was reminded to clear them.	*Follow-up action was needed for the item.
	30/10/2008	Standing water with remaining oil was observed at underneath of air compressor at Western Portal. The Contractor was reminded to clear them properly.	*Follow-up action was needed for the item.
<b><i>Air Quality</i></b>	10/10/2008	Dark smoke was observed emitted from the generator at Western Portal. The Contractor was reminded to provide well maintenance for the plant equipments.	Rectification/improvement was observed during the follow-up audit session.
	15/10/2008	Dusty unpaved area was observed at Western Portal. The Contractor was reminded to provide water spray more frequently.	Rectification/improvement was observed during the follow-up audit session.
	30/10/2008	Dry unpaved area was observed at Western Portal. The Contractor was reminded to provide water spray to control dust emission.	Rectification/improvement was observed during the follow-up audit session.
<b><i>Noise</i></b>	15/10/2008	Noise from water pump was noticed at Intake TP5. The Contractor was reminded to provide noise control measures to minimize noise nuisance.	The item was not observed during the follow-up audit session.
	22/10/2008	Noise from water pump was noticed at Intake TP4. The Contractor was reminded to provide noise control measures to minimize noise nuisance.	The item was not observed during the follow-up audit session.
	30/10/2008	Noise from GI works was noticed at Intake RR1. The Contractor was reminded to provide noise control measures to minimize noise to the nearest residents.	The item was not rectified during the follow-up audit session.
<b><i>Waste / Chemical Management</i></b>	10/10/2008	Oil leakage was observed from the loader at Eastern Portal. The Contractor was reminded to clear them and well maintained the	The item was not observed during the follow-up audit session.

Parameters	Date	Observations and Recommendations	Follow-up
		equipment.	
	15/10/2008	Oil leakage was observed from the loader at Eastern Portal. The Contractor was reminded to clear them and well maintained the equipment.	Rectification/improvement was observed during the follow-up audit session.
	22/10/2008	General refuses was observed at Intake TP5. The Contractor was reminded to clear them.	The item was not observed during the follow-up audit session.
	22/10/2008	Oil leakage with standing water at underneath of air compressor was observed at Western Portal. The Contractor was reminded to clear them properly.	*Follow-up action was needed for the item.
	22/10/2008	Remaining oil was observed at the oil drum at Western Portal. The Contractor was reminded to clear them properly.	Rectification/improvement was observed during the follow-up audit session.
	30/10/2008	Standing water with remaining oil was observed at underneath of air compressor at Western Portal. The Contractor was reminded to clear them properly.	*Follow-up action was needed for the item.
<b>Ecology</b>	10/10/2008	Milky water was observed discharging to the existing stream at Intake W3. The Contractor was reminded to provide mitigation measures to prevent any wastewater from running to the stream.	Rectification/improvement was observed during the follow-up audit session.
	15/10/2008	Silty water was observed discharging to the existing stream at Intake TP4. The Contractor was reminded to provide mitigation measures to prevent any wastewater from running to the stream.	Rectification/improvement was observed during the follow-up audit session.
	30/10/2008	Worm sand bags were observed at the access road at Eastern Portal near existing stream. The Contractor was reminded to replace them.	*Follow-up action was needed for the item.
<b>Reminders</b>	10/10/2008	The Contractor was reminded of the followings: - Clear all standing water in the label bag that secure around the trees at Eastern and Western Portal Sites.	*Follow-up action was needed for the item.
	15/10/2008	The Contractor was reminded of the followings: - Clear all standing water in the label bag that secure around the trees at Eastern Portal, Western Portal and Intake sites.	*Follow-up action was needed for the item.
	22/10/2008	The Contractor was reminded of the followings: - Clear all standing water in the label bag that secure around the trees at Eastern Portal, Western Portal and Intake sites.	*Follow-up action was needed for the item.
	30/10/2008	The Contractor was reminded of the followings: - Keep clear the standing water in the label bags that secure around the trees at Eastern, Western and Intake sites.	*Follow-up action was needed for the item.

Note: (\*) The Environmental deficiencies have been rectified by the Contractor. However, the item was reoccurred during the follow-up site audit due to construction activities/rainstorm. The Contractor was reminded to rectify the deficiencies more frequently.

5.9 The monthly IEC audit was carried out on 30<sup>th</sup> October 2008, the observations were recorded and they are presented as follows:

5.10 Follow-up and rectification works in response to IEC observations on 26 September 2008 were satisfied.

30<sup>th</sup> October 2008

Intake RR1

- Oil leakage was observed on site. Prompt cleaning is needed.
- Noise from GI works was likely exceeding the noise limit of 75dB(A) at nearest NSR (Merry Court). Noise mitigation measures should be sought.

Eastern Portal

- Water seepage from bottom of hoarding was observed. Prompt rectification is needed.

Eastern & Western Portal

- Stagnant water was observed on site. More frequent cleaning up is required.

Western Portal

- Wet soil was mixed with oil in the drip trays of generators. More frequent removal of oil contaminated soil is necessary. The soil should be treated as chemical waste.
- Bare ground was dry. More frequent watering is needed.
- The surface channel under elevated road was blocked by construction material. The purpose of channel was for directing surface runoff from elevated road. Prompt cleaning of materials from the channel is required on a separate drain/channel for uncontaminated surface runoff is needed.
- Chemical drums were placed on paved area next to wheel washing bay. Prompt storage of chemicals according to EPD's code of practice for chemical storage is necessary.

**Non-compliance Recorded during Site Inspections**

5.11 No non-compliance was recorded in the reporting month.

**Summary of Mitigation Measures Implemented**

5.12 The Contractor has implemented the mitigation measures as recommended in the EIA and the updated EM&A Manual in the reporting period except those mitigation measures not applicable at this stage. Status of the implementation of mitigation measures is presented in Table 1.2 and **Appendix L**.

5.13 According to the updated EM&A Manual and EP condition, mitigation measures such as noise enclosure and use of quiet PME are required to be implemented.

5.14 The actual implementation status of major mitigation measures required under the EP is as follows:

- Installation of silt curtain during the course of marine works.
- Design of noise enclosure at Eastern Portal.
- Submitted the Alternative Plant Inventory (EP condition 2.8(c)).



5.15 An updated summary of the EMIS is provided in **Appendix L**.

**Implementation Status of Event Action Plans**

5.16 The Event Action Plans for air quality and noise are presented in **Appendix M**.

*Eastern Portal*

1-hr TSP Monitoring

5.17 No Action/Limit Level exceedance was recorded in the reporting month.

24-hr TSP Monitoring

5.18 No Action/Limit Level exceedance was recorded in the reporting month.

Construction Noise

5.19 No Action/Limit Level exceedance was recorded in the reporting month.

*Western Portal*

1-hr TSP Monitoring

5.20 No Action/Limit Level exceedance was recorded in the reporting month.

24-hr TSP Monitoring

5.21 No Action/Limit Level exceedance was recorded in the reporting month.

Construction Noise

5.22 No Action/Limit Level exceedance was recorded for construction noise.

Water Quality

5.23 No Action/Limit Level exceedance was recorded for water quality.

**Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution**

5.24 Three environmental complaints were received in the reporting month. For the details, please refer to the following table: -

<b>Complaint No.</b>	<b>Date</b>	<b>Complaint Details</b>
COM-2008-10-011	11 October 2008	The complaint was lodged by one of the resident of Victoria Road, Ms Cheung on 11 October regarding about the noise nuisance generated from the construction works at Western Portal
COM-2008-10-012	15 October 2008	The complaint was lodged by Mr Choi on 15 October 2008 regarding about the noise generated from the GI works, which starts from 8:30 hrs to 17:30 hrs next to Aigburth at May Road.
COM-2008-10-013	31 October 2008	The complaint was lodged by Mr Lai on 31 October 2008 regarding the black smoke is emitted and noise is generated from the machine at the site (Intake TP5), he needed to close the windows to prevent the black smoke from entering his flat and to attenuate the noise.

- 5.25 No warning, summon and notification of successful prosecution was received in the reporting month.
- 5.26 There were a total of 6 environmental complaints, no warning, summons and successful prosecution received since the commencement of the Project. The Complaint Log is attached in **Appendix N**.

**6. FUTURE KEY ISSUES**

**Key Issues for the Coming Month**

6.1 Key environmental issues at both Eastern and Western Portals in the coming month include:

*Both Eastern and Western Portal*

- Noise from operation of the equipment, especially for rock-breaking activities and machinery on-site;
- Dust generation from stockpiles of dusty materials, excavation works and rock breaking activities;
- Runoff from exposed slope;
- Wastewater and runoff discharge from site;
- Regular removal of silt, mud and sand along u-channels and sedimentation tanks;
- Review and implementation of temporary drainage system for the surface runoff;
- Proper storage of construction materials on site;
- Storage of chemicals/fuel and chemical waste/waste oil on site;
- Watering for rock breaking activity, soil nailing and on haul road;
- Accumulation of general and construction waste on site.

*Only at Western Portal*

- Contamination of marine water.

6.2 The tentative program of major site activities and the impact prediction and control measures for the coming two month, i.e. November 2008 to December 2008 are summarized as follows:

Construction Works	Major Impact Prediction	Control Measures
- Main tunnel excavation, intake shaft and temporary access road construction at Eastern Portal. - Shallow & deep excavation works, arch tunnel excavation works and marine works	Air impact (dust)	a) Frequent watering of haul road and unpaved/exposed areas; b) Frequent watering or covering stockpiles with tarpaulin or similar means; and c) Watering of any earth moving activities.
	Water quality impact (marine and surface run-off)	d) Diversion of the collected effluent to de-silting facilities for treatment prior to discharge to public storm water drains; e) Provision of adequate de-silting facilities for treating surface run-off and other collected effluents prior to discharge; f) Provision of perimeter protection such as sealing of hoarding footings to avoid run-off from entering the existing storm water drainage system via public road; and g) Provision of measures to prevent discharge into the stream. h) Installation and maintenance of silt curtain

Construction Works	Major Impact Prediction	Control Measures
at Western Portal. - Utilities trial pits and additional ground investigation works at 12 nos. Intake sites. - Cofferdam construction at Intake W0.	Noise Impact	i)Scheduling of noisy construction activities if necessary to avoid persistent noisy operation; j)Controlling the number of plants use on site; k) Regular maintenance of machines; and l) Use of acoustic barriers if necessary.

**Monitoring Schedule for the Next Month**

6.3 The tentative environmental monitoring schedules for the next month are shown in **Appendix D**.

**Construction Program for the Next Month**

6.4 The tentative construction program for the Project is provided in **Appendix O**.

## 7. CONCLUSIONS AND RECOMMENDATIONS

### Conclusions

- 7.1 Environmental monitoring works were performed in the reporting period and all monitoring results were checked and reviewed.

#### 1-hr TSP Monitoring

- 7.2 All 1-hr TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### 24-hr TSP Monitoring

- 7.3 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Construction Noise Monitoring

- 7.4 All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Water Quality

- 7.5 All water quality monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Complaint and Prosecution

- 7.6 No environmental complaints and environmental prosecution were received in the reporting month.

### Recommendations

- 7.7 According to the environmental audit performed in the reporting period, the following recommendations were made:

#### *Air Quality Impact*

- To prohibit any open burning on site.
- To regularly maintain the machinery and vehicles on site.
- To implement dust suppression measures on all haul roads, stockpiles, dry surfaces and excavation works.
- To provide hoarding

*Noise Impact*

- To inspect the noise sources inside the site.
- To space out noisy equipment and position the equipment as far away as possible from sensitive receivers.
- To provide temporary noise barriers for operations of noisy equipment near the noise sensitive receivers in an appropriate location.

*Water Impact*

- To prevent any surface runoff discharge into any stream course.
- To review and implement temporary drainage system.
- To identify any wastewater discharges from site.
- To ensure properly maintenance for de-silting facilities.
- To clear the silt and sediment in the sedimentation tanks.
- To review the capacity of de-silting facilities for discharge.
- To divert all the water generated from construction site to de-silting facilities with enough handling capacity before discharge.
- To avoid accumulation of stagnant and ponding water on site.

*Waste/Chemical Management*

- To check for any accumulation of waste materials or rubbish on site.
- To ensure the performance of sorting of C&D materials at source (during generation);
- To carry out inspection of dump truck at site exit to ensure inert and non-inert C&D materials are properly segregated before removing off site.
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the site.
- To avoid improper handling or storage of oil drum on site.


---


---

## FIGURES


---

---

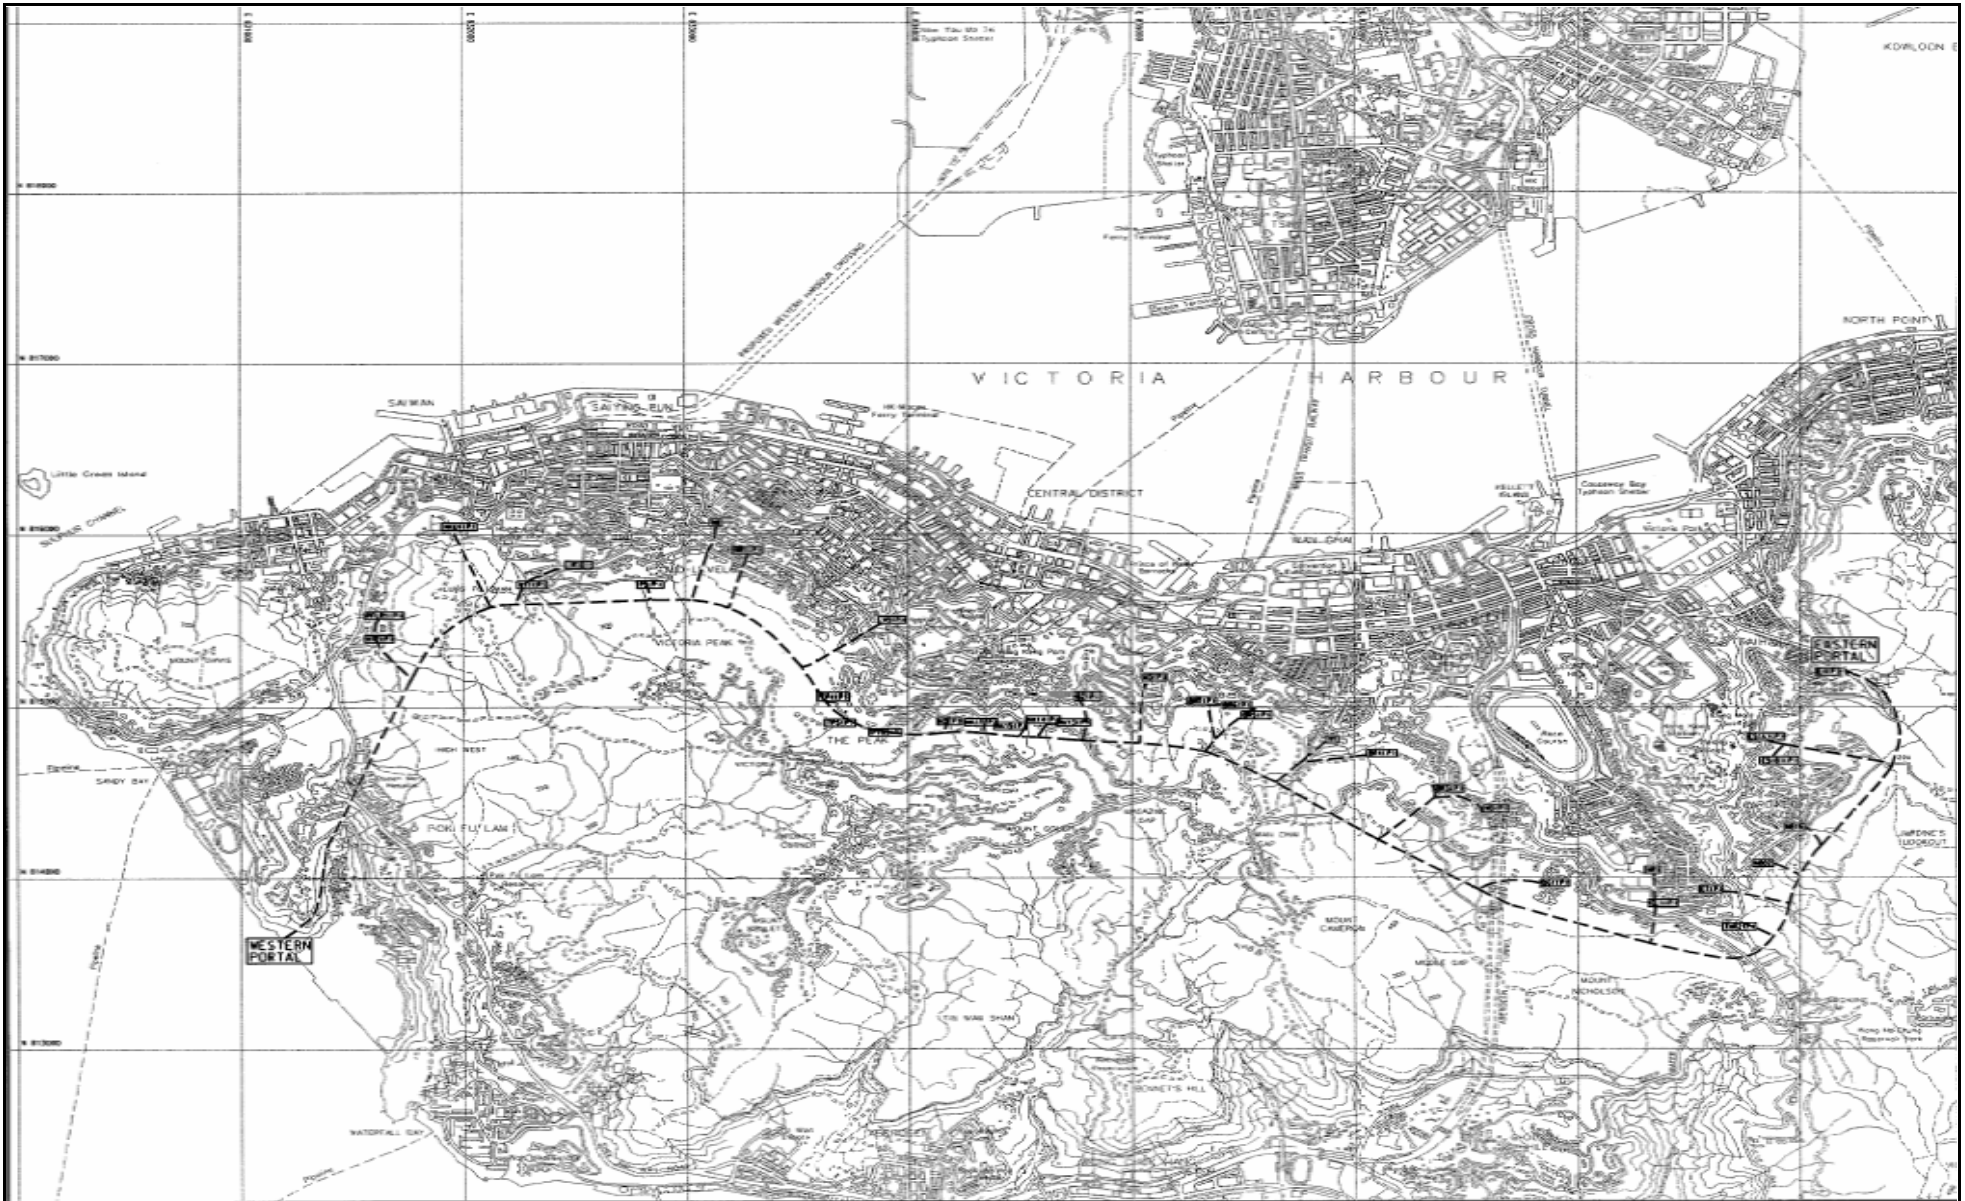


Title	Contract No. DC/2007/10		Scale	Propo:	
	Design and Construction of Hong Kong West Drainage Tunnel		N.T.S	No. MA8001	
	Site Layout Plan		Date	Figure	
			Apr-08	1.1	



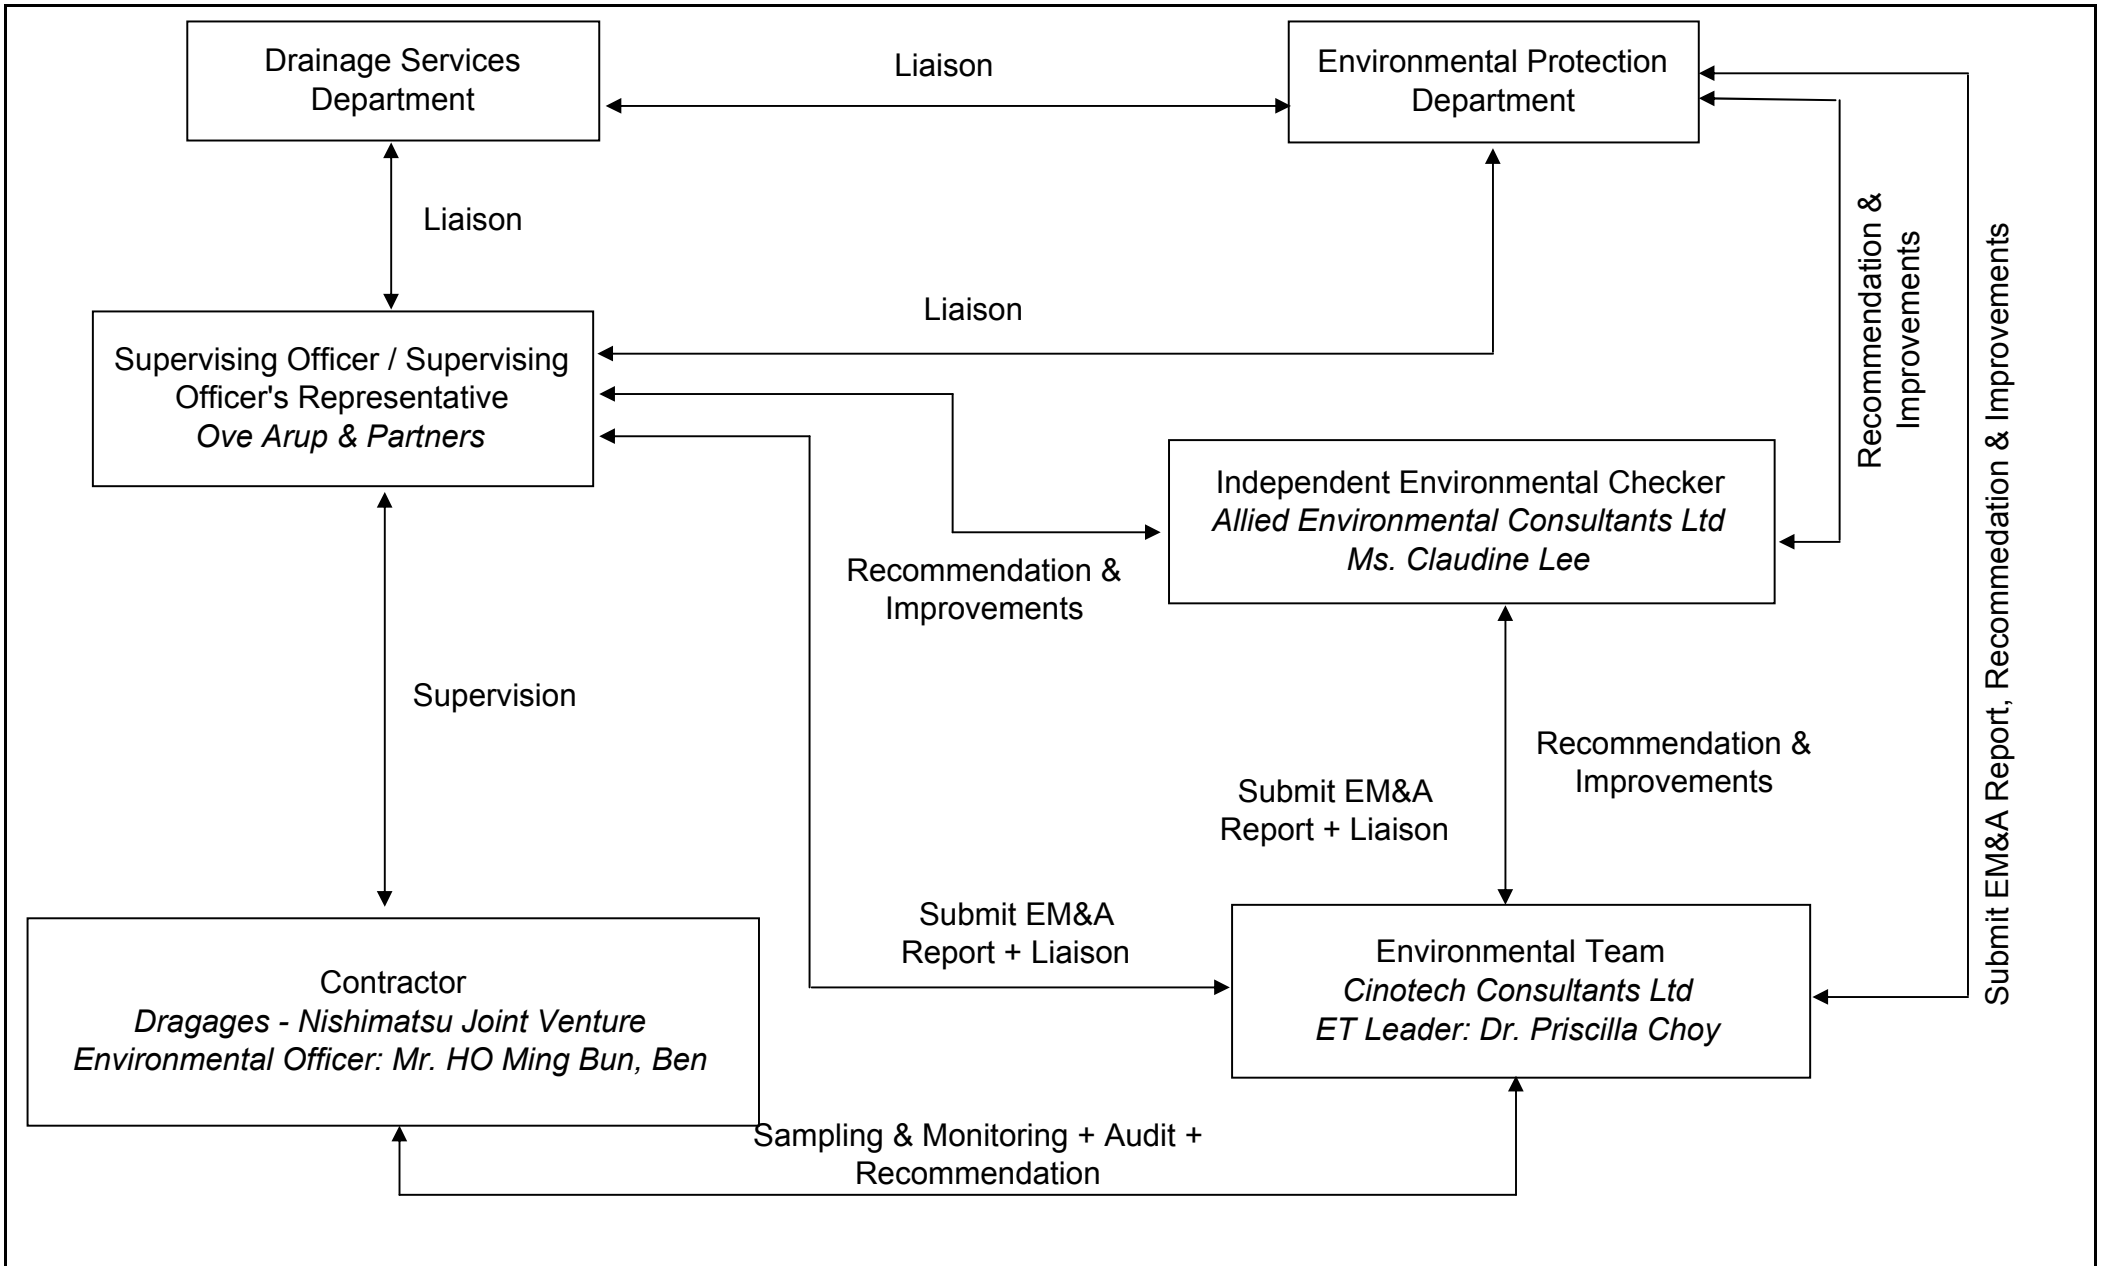

Title	Contract No. DC/2007/10		Scale	Proposa
	Design and Construction of Hong Kong West Drainage Tunnel		N.T.S	No. MA8001
Organization Chart		Date	Apr-08	Figure 2.1



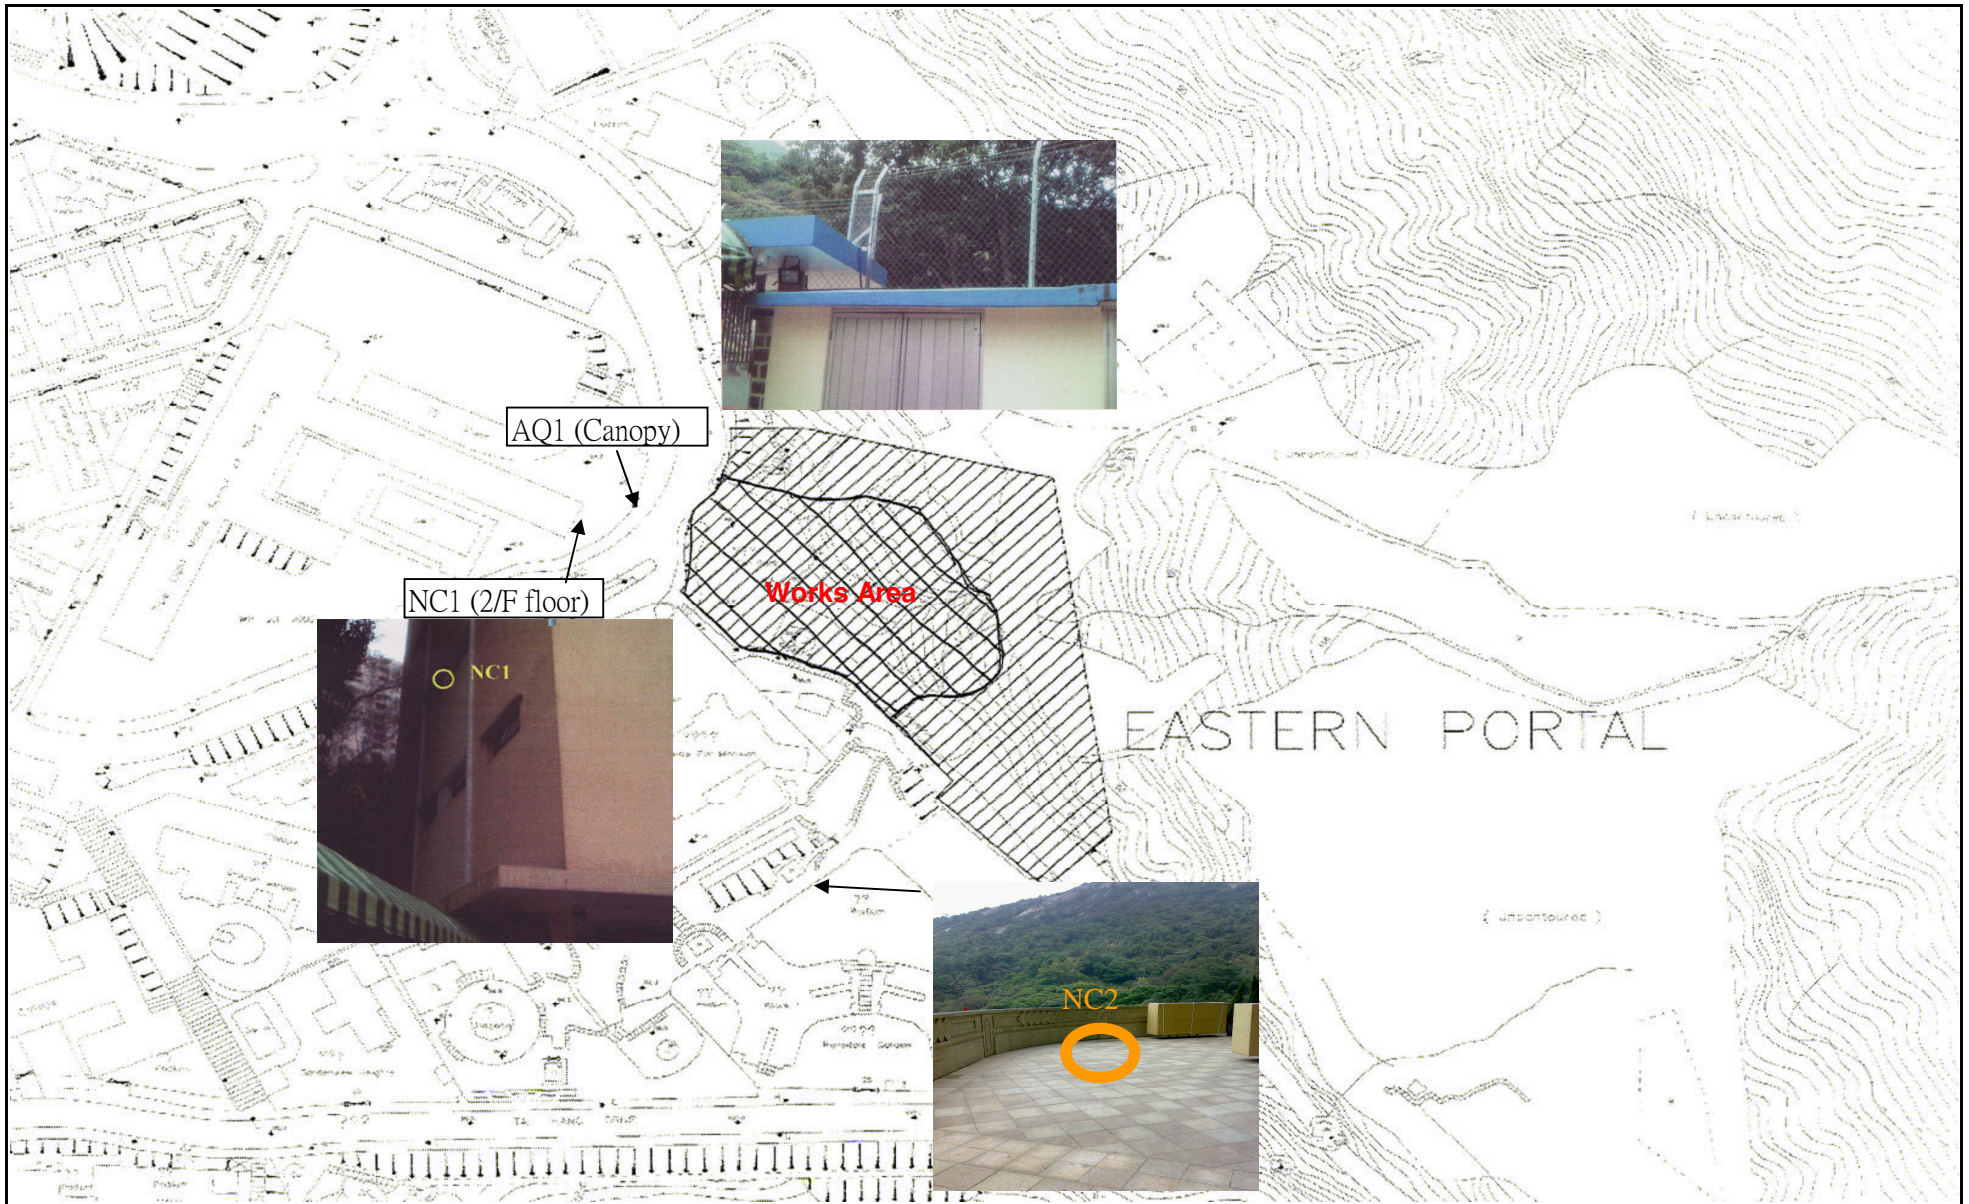


Title	Contract No. DC/2007/10		Scale	Propos
	Design and Construction of Hong Kong West Drainage Tunnel (Eastern Portal)		N.T.S	No. MA8001
	Locations of Air Quality and Noise Monitoring Station		Date	Figure
			Jun-08	3.1a

**CINOTECH**



Title <b>Contract No. DC/2007/10</b> <b>Design and Construction of Hong Kong West Drainage Tunnel</b> <b>(Western Portal)</b> <b>Locations of Air Quality and Noise Monitoring Station</b>	Scale N.T.S	Propos No. MA8001	
	Date Jun-08	Figure 3.1b	

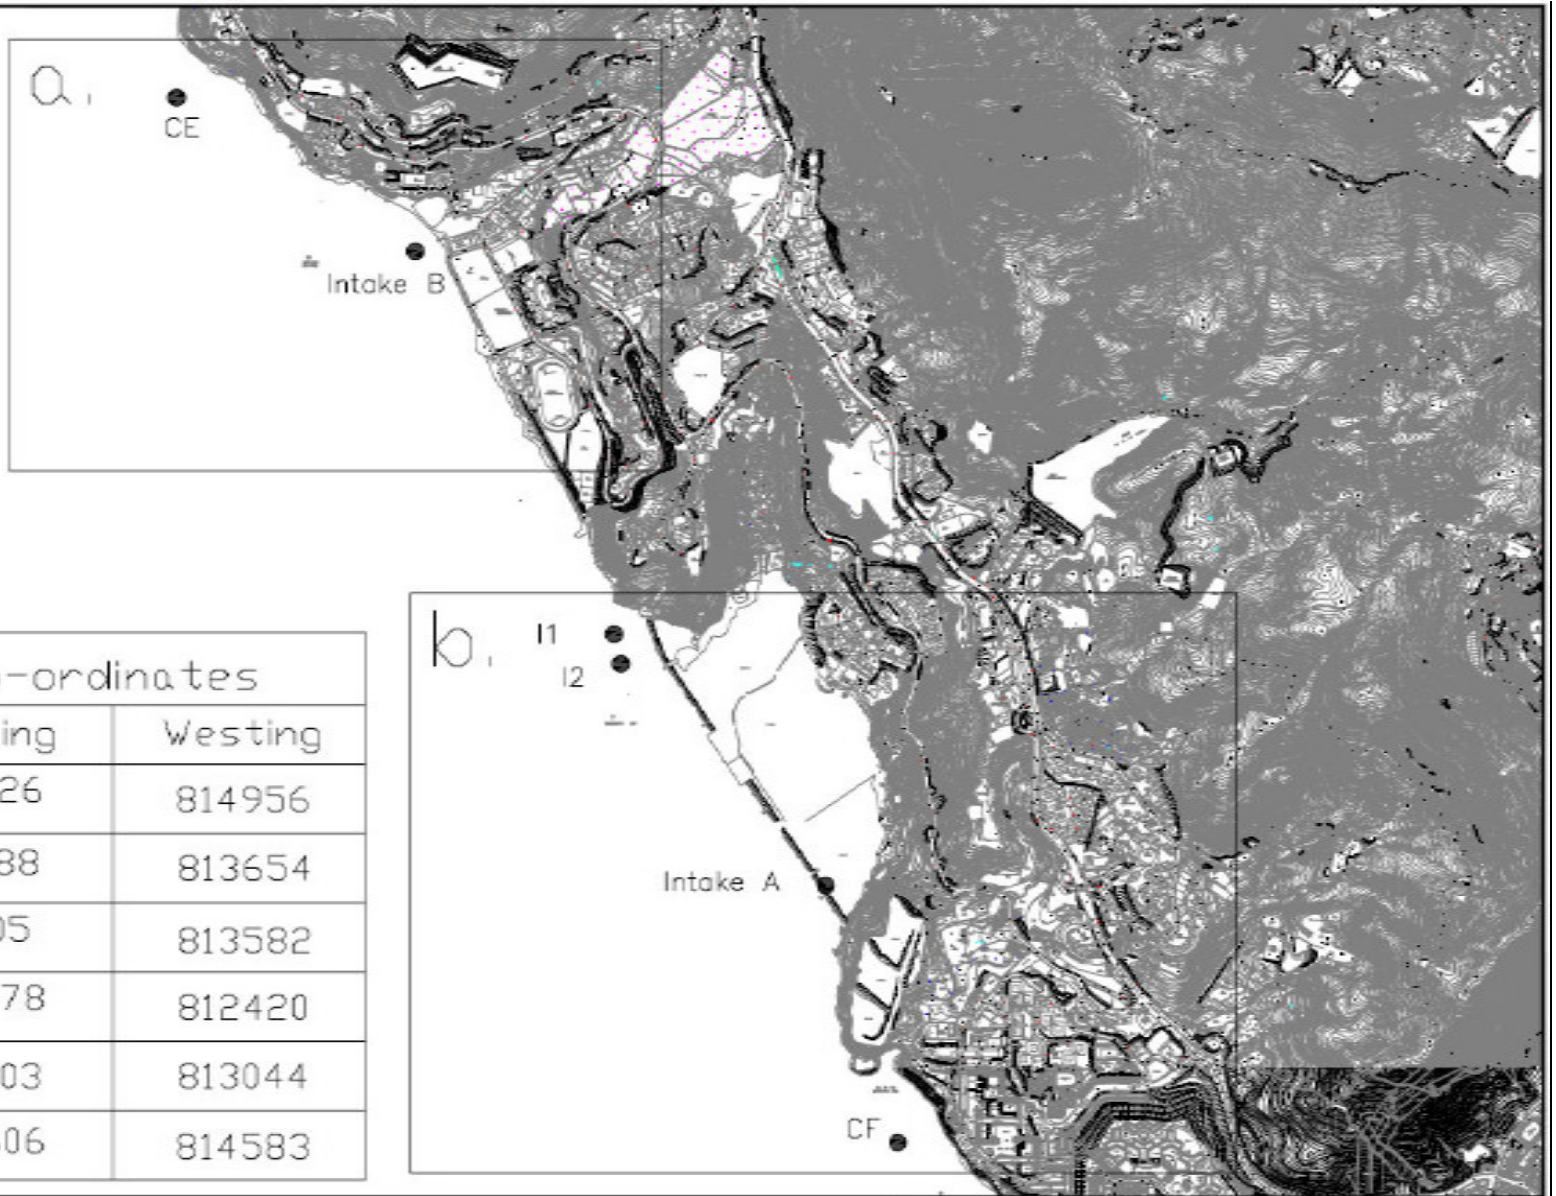

Point No.	Co-ordinates	
	Easting	Westing
CE	830026	814956
I1	831088	813654
I2	831105	813582
CF	831778	812420
Intake A	831603	813044
Intake B	830606	814583

Title Contract No. DC/2007/10  
Design and Construction of Hong Kong West Drainage Tunnel

Locations of Water Quality Monitoring Stations


Scale  
N.T.S

Date  
Jun-08

Propos  
No. MA8001

Figure  
4.1


CINOTECH

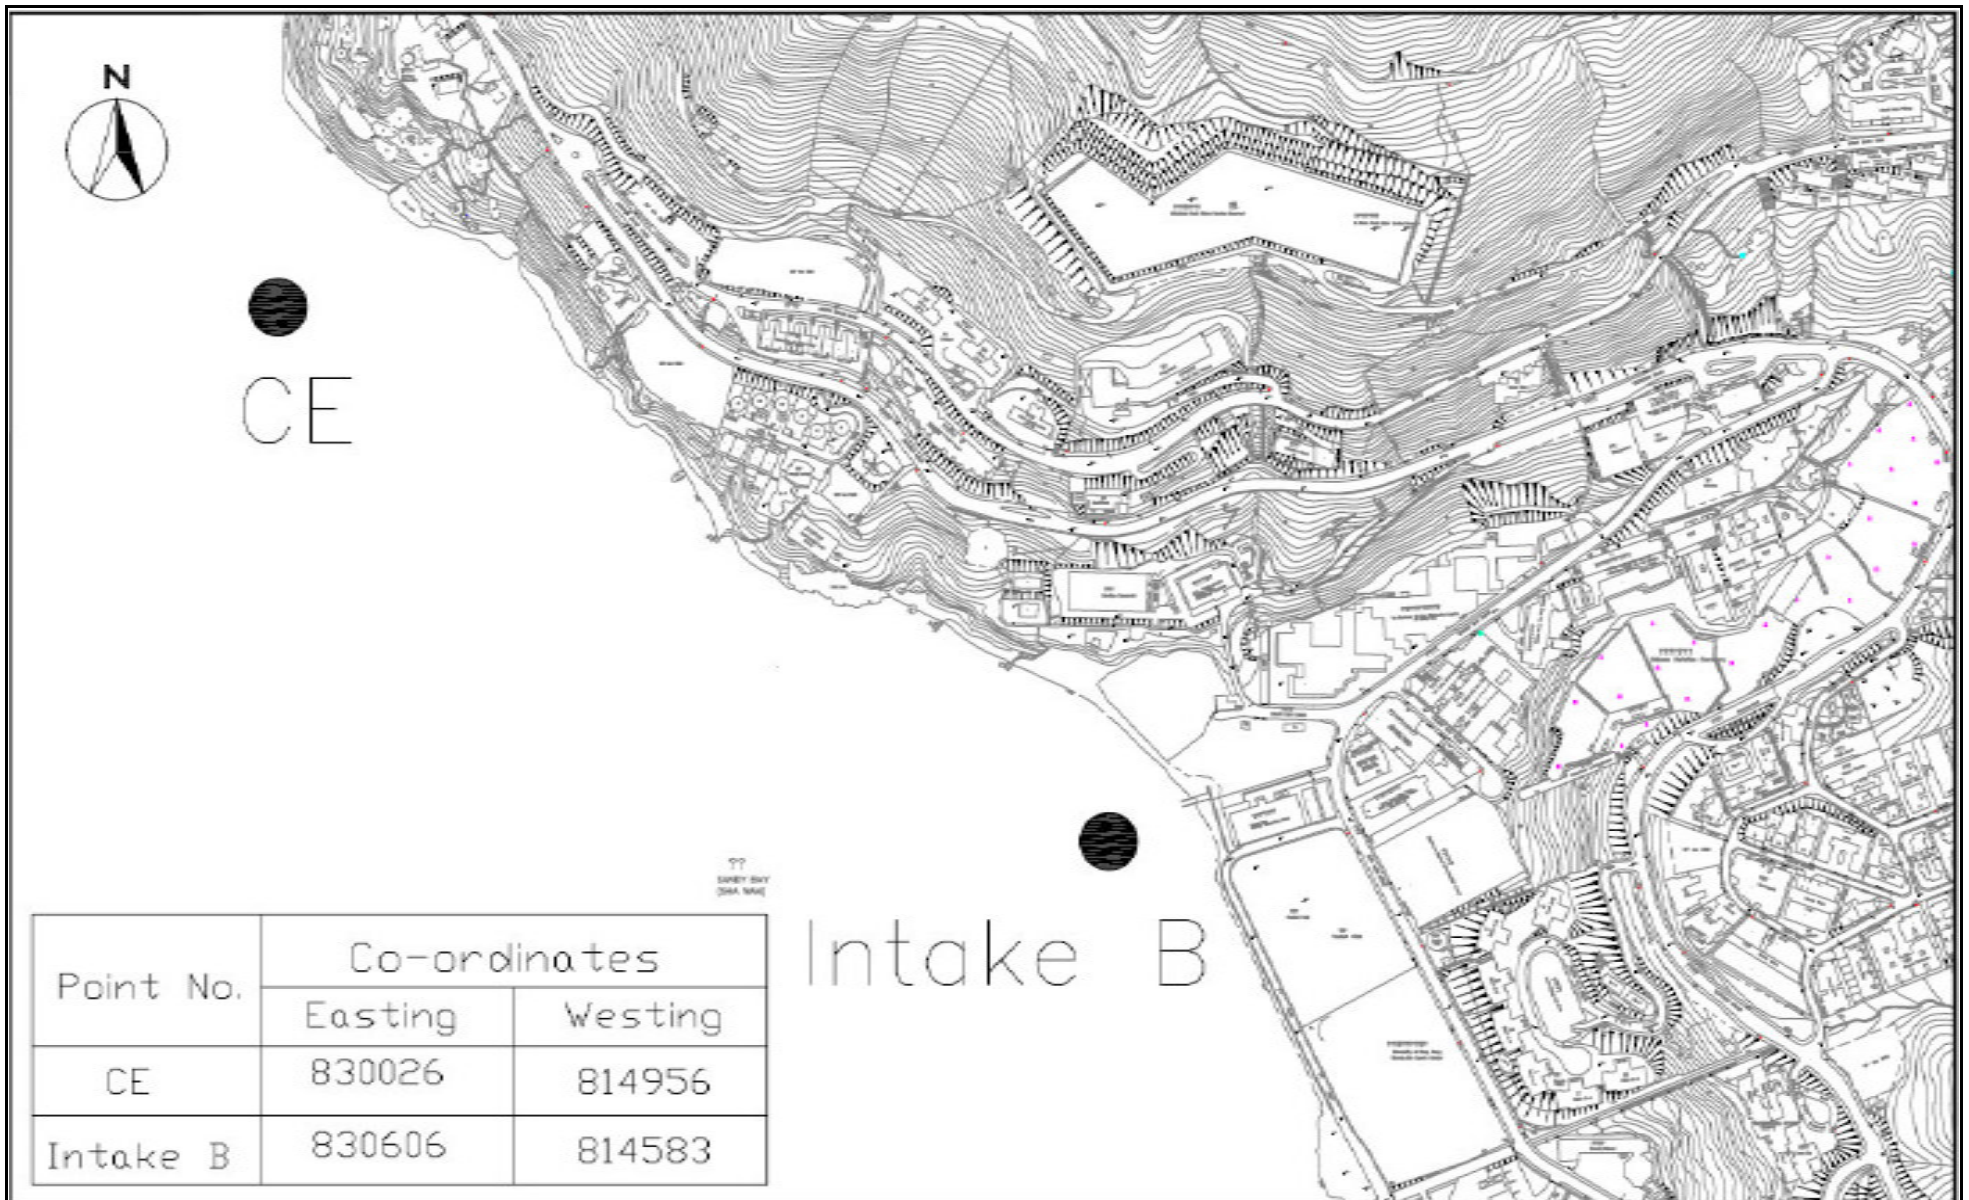


Title Contract No. DC/2007/10  
 Design and Construction of Hong Kong West Drainage Tunnel  
 Locations of Water Quality Monitoring Stations


Scale	N.T.S	Propos No.	MA8001
Date	Jun-08	Figure	4.1a



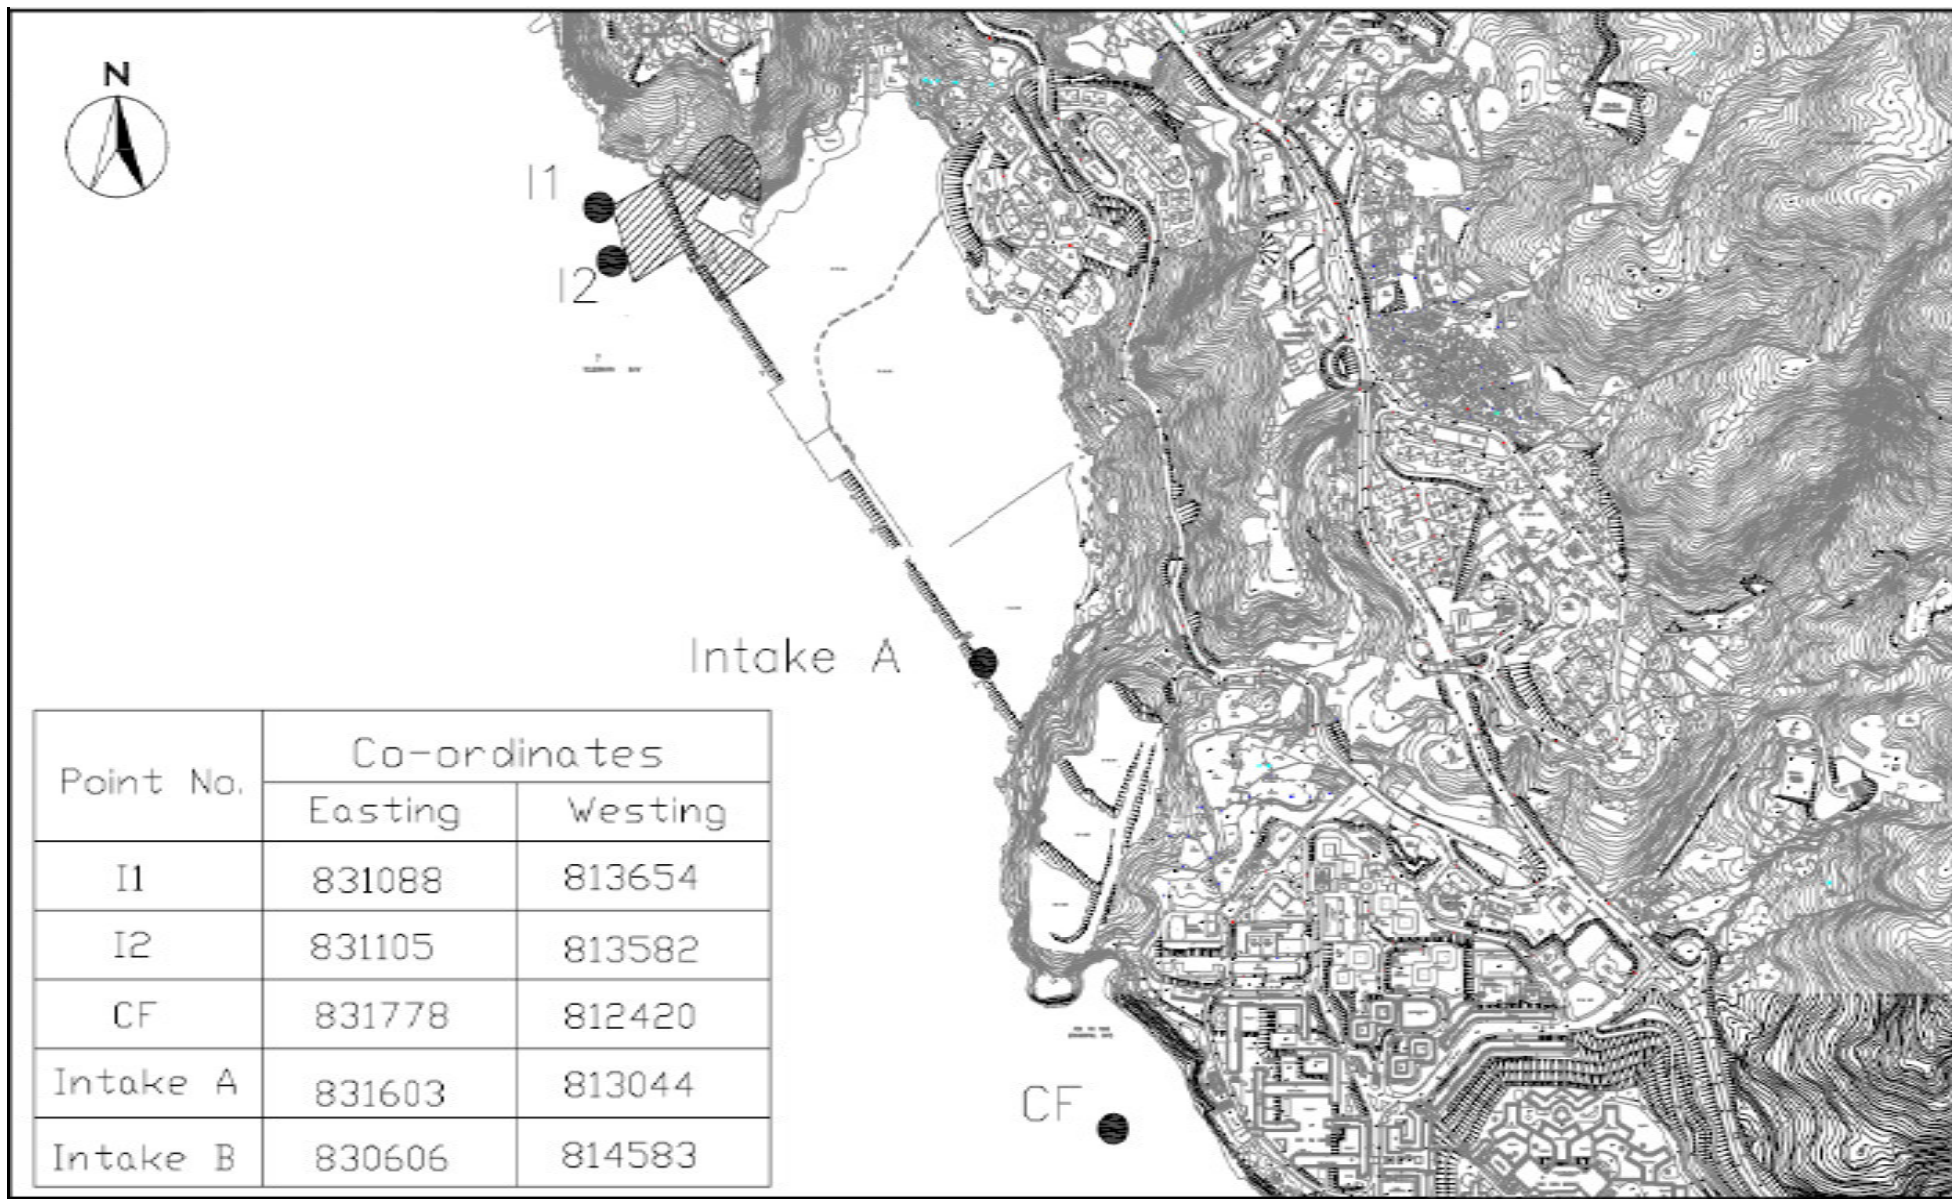

Point No.	Co-ordinates	
	Easting	Westing
I1	831088	813654
I2	831105	813582
CF	831778	812420
Intake A	831603	813044
Intake B	830606	814583

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel Locations of Water Quality Monitoring Stations	Scale	Propos	
		N.T.S	
	Date	Figure	
	Jun-08	4.1b	

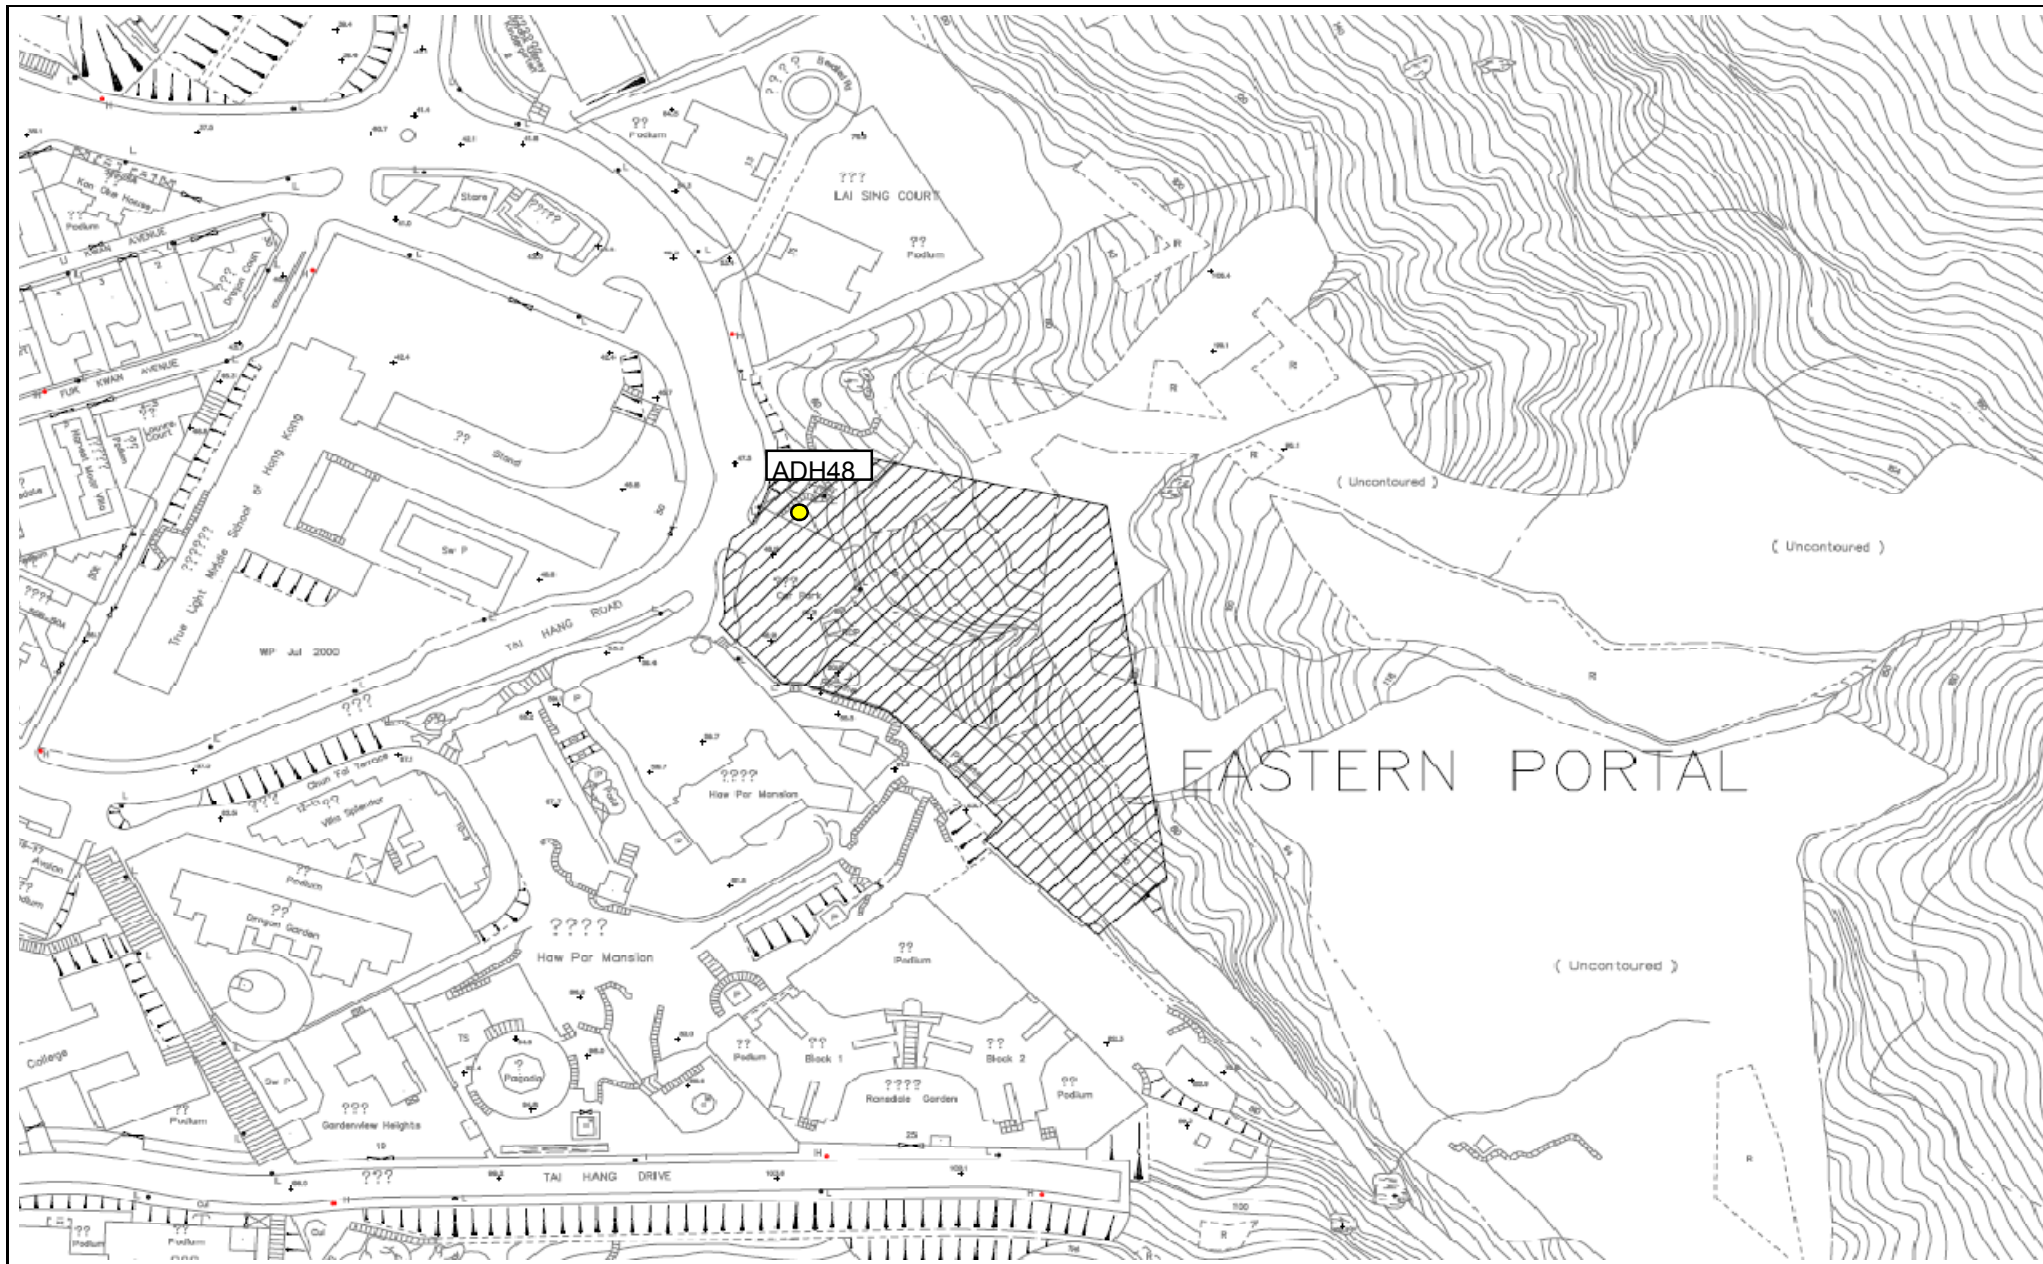

Title	Contract No. DC/2007/10		Scale	Propos	CINOTECH
	Design and Construction of Hong Kong West Drainage Tunnel (Eastern Portal)			N.T.S	
	Location of ground water level Monitoring Station		Date	Figure	
			Jun-08	4.2	

---

---

**APPENDIX A  
ACTION AND LIMIT LEVELS**

---

---



## Appendix A - Action and Limit Levels

**Table A-1 Action and Limit Levels for 1-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AQ1	345	500
AQ2	321	

**Table A-2 Action and Limit Levels for 24-Hour TSP**

Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AQ1	201	260
AQ3	156	

**Table A-3 Action and Limit Levels for Construction Noise**

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75* dB(A)
0700-2300 hrs on holidays; and 1900-2300 hrs on all other days		60/65/70** dB(A)
2300-0700 hrs of next day		45/50/55** dB(A)

(\*) reduce to 70 dB(A) for schools and 65 dB(A) during school examination periods.

(\*\*) to be selected based on Area Sensitivity Rating.

**Table A-4 Action and Limit Levels for Water Quality**

Parameter		Action	Limit
DO, mg/L	Surface and Middle	6.3	6.2
	Bottom	6.0	5.8
SS, mg/L		15.7 or 120% of upstream control station's SS at the same tide of the same day	16.4 or 130% of SS readings at the upstream control station at the same tide of same day and specific sensitive receiver water quality requirements
Turbidity, NTU		10.2 or 120% of upstream control station's turbidity at the same tide of the same day	11.1 or 130% of turbidity at the upstream control station at the same tide of same day

---

---

**APPENDIX B  
COPIES OF CALIBRATION  
CERTIFICATES**

---

---

# High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

**CINOTECH**

File No. MA8001/44/0004

Station AQ1 - True Light Middle School of Hong Kong Operator: WK  
 Date: 15-Aug-08 Next Due Date: 14-Oct-08  
 Equipment No.: A-01-44 Serial No. 1316

Ambient Condition			
Temperature, Ta (K)	302.6	Pressure, Pa (mmHg)	756

Orifice Transfer Standard Information					
Equipment No.:	A-04-06	Slope, mc	0.0575	Intercept, bc	0.0395
Last Calibration Date:	10-Mar-08	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	9-Mar-09	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of oil	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.2	3.46	59.44	8.7	2.92
2	10.2	3.16	54.29	7.2	2.66
3	7.0	2.62	44.85	5.0	2.21
4	5.1	2.24	38.19	3.1	1.74
5	3.1	1.74	29.62	1.8	1.33

By Linear Regression of Y on X  
 Slope, mw = 0.0540 Intercept, bw = -0.2741  
 Correlation coefficient\* = 0.9981  
 \*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM  
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point;  $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.28

Remarks: \_\_\_\_\_

Conducted by: Wk Tang Signature: \_\_\_\_\_ Date: 15/8/08  
 Checked by: [Signature] Signature: \_\_\_\_\_ Date: 15 Aug 2008

# High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

**CINOTECH**

File No. MA8001/44/0005

Station AQ1 - True Light Middle School of Hong Kong Operator: WK  
 Date: 14-Oct-08 Next Due Date: 13-Dec-08  
 Equipment No.: A-01-44 Serial No. 1316

Ambient Condition			
Temperature, Ta (K)	298.9	Pressure, Pa (mmHg)	765.4

Orifice Transfer Standard Information					
Equipment No.:	A-04-06	Slope, mc	0.0575	Intercept, bc	0.0395
Last Calibration Date:	10-Mar-08	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	9-Mar-09	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	ΔH (orifice), in. of water	[ΔH x (Pa/760) x (298/Ta)] <sup>1/2</sup>	Qstd (CFM) X - axis	ΔW (HVS), in. of oil	[ΔW x (Pa/760) x (298/Ta)] <sup>1/2</sup> Y-axis
1	12.3	3.51	60.43	8.5	2.92
2	10.7	3.28	56.32	7.1	2.67
3	7.6	2.76	47.36	4.7	2.17
4	5.3	2.31	39.43	3.2	1.79
5	3.0	1.74	29.50	1.8	1.34

By Linear Regression of Y on X

Slope, mw = 0.0509 Intercept, bw = -0.1924

Correlation coefficient\* = 0.9984

\*If Correlation Coefficient < 0.990, check and recalibrate.

### Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = (mw x Qstd + bw)<sup>2</sup> x (760 / Pa) x (Ta / 298) = 3.97

Remarks: \_\_\_\_\_

Conducted by: WK Tang Signature: [Signature] Date: 14/10/08  
 Checked by: [Signature] Signature: [Signature] Date: 14 Oct 2008







TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE.  
 VILLAGE OF CLEVELAND, OH 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX  
 WWW.TISCH-ENVY.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Mar 10, 2008 Rootsometer S/N 9833640 Ta (K) - 295  
 Operator Tisch Orifice I.D. - 0999 Pa (mm) - 746.76

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3890	3.2	2.00
2	NA	NA	1.00	0.9850	6.3	4.00
3	NA	NA	1.00	0.8810	7.8	5.00
4	NA	NA	1.00	0.8410	8.6	5.50
5	NA	NA	1.00	0.6950	12.5	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9917	0.7139	1.4113	0.9957	0.7168	0.8874
0.9876	1.0026	1.9959	0.9916	1.0067	1.2549
0.9854	1.1185	2.2315	0.9894	1.1231	1.4030
0.9844	1.1706	2.3405	0.9884	1.1753	1.4715
0.9792	1.4090	2.8227	0.9832	1.4147	1.7747
Qstd slope (m) = 2.03154			Qa slope (m) = 1.27212		
intercept (b) = -0.03970			intercept (b) = -0.02496		
coefficient (r) = 0.99999			coefficient (r) = 0.99999		

y axis =  $\text{SQRT}[\text{H2O}(\text{Pa}/760)(298/\text{Ta})]$

y axis =  $\text{SQRT}[\text{H2O}(\text{Ta}/\text{Pa})]$

CALCULATIONS

$V_{std} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/760](298/\text{Ta})$   
 $Q_{std} = V_{std}/\text{Time}$

$V_a = \text{Diff Vol}[(\text{Pa} - \text{Diff Hg})/\text{Pa}]$   
 $Q_a = V_a/\text{Time}$


For subsequent flow rate calculations:

$Q_{std} = 1/m\{[\text{SQRT}(\text{H2O}(\text{Pa}/760)(298/\text{Ta}))] - b\}$   
 $Q_a = 1/m\{[\text{SQRT}(\text{H2O}(\text{Ta}/\text{Pa}))] - b\}$



TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE.  
 VILLAGE OF CLEVELAND, OH 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX  
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

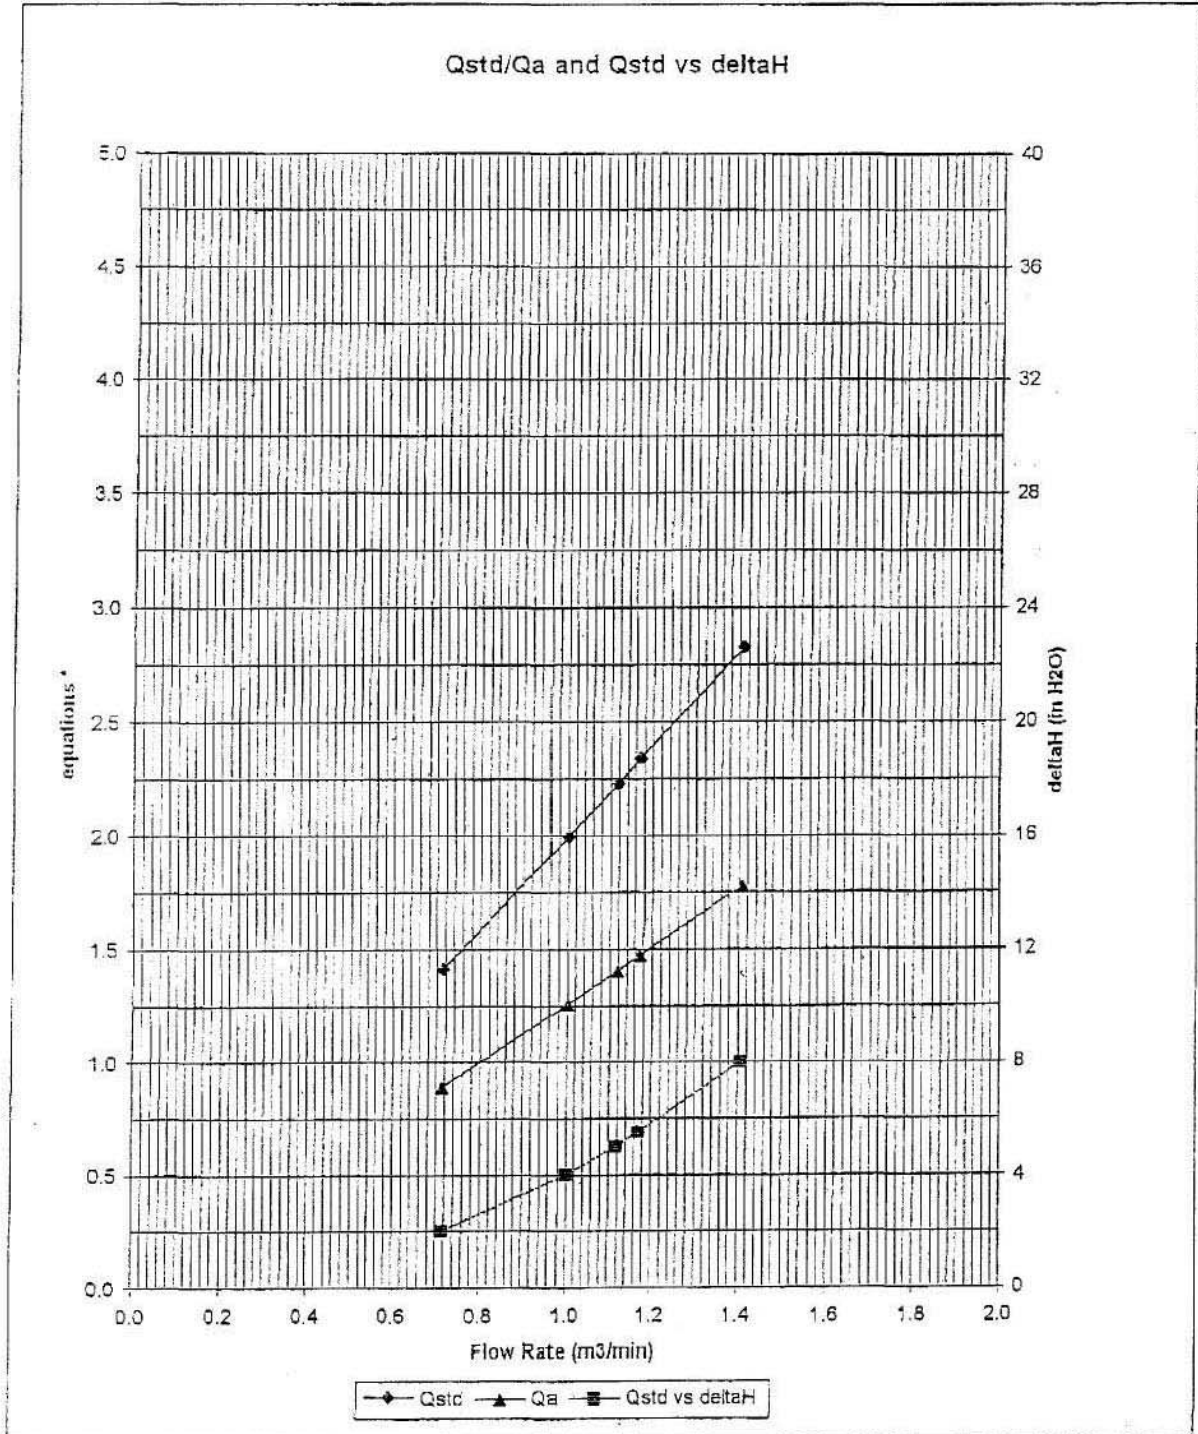

\* y-axis equations:

Qstd series: 
$$\sqrt{\Delta H \left( \frac{P_a}{P_{std}} \right) \left( \frac{T_{std}}{T_a} \right)}$$

Qa series: 
$$\sqrt{(\Delta H (T_a / P_a))}$$



## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/07/80502
Date of Issue:	2008-05-03
Date Received:	2008-05-02
Date Tested:	2008-05-02
Date Completed:	2008-05-03
Next Due Date:	2009-05-02

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description : RS232 Integral Vane Digital Anemometer  
Manufacturer : AZ Instrument  
Model No. : 451104  
Serial No. : 9020746  
Equipment No. : A-03-01

**Test conditions:**

Room Temperature : 21 degree Celsius  
Relative Humidity : 65%  
Pressure : 101.3 kPa

**Methodology:**

The anemometer has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

	Reference Set Point	Instrument Readings
Measuring Air Velocity, m/s	2.00	2.00
Temperature, °C	21.0	21.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

**TEST REPORT**

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/080823/1B
Date of Issue:	2008-08-23
Date Received:	2008-08-22
Date Tested:	2008-08-23
Date Completed:	2008-08-23
Next Due Date:	2008-10-22

**ATTN:** Mr. Henry Leung

Page: 1 of 1

**Certificate of Calibration**

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3
Serial No.	: 281835
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 666 CPM
Equipment No.	: A-02-02

**Test Conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 62%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0037
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**  
*Laboratory Manager*

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/081023/1B
Date of Issue:	2008-10-23
Date Received:	2008-10-22
Date Tested:	2008-10-23
Date Completed:	2008-10-23
Next Due Date:	2008-12-22

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3
Serial No.	: 281835
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 666 CPM
Equipment No.	: A-02-02

**Test Conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 62%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0038
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
\_\_\_\_\_  
**PATRICK TSE**  
Laboratory Manager

**TEST REPORT**

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/080918/1
Date of Issue:	2008-09-18
Date Received:	2008-09-17
Date Tested:	2008-09-18
Date Completed:	2008-09-18
Next Due Date:	2008-11-17

**ATTN:** Mr. Henry Leung

Page: 1 of 1

**Certificate of Calibration**

**Item for Calibration:**

Description	: Laser Dust Monitor
Manufacturer	: Sibata
Model No.	: LD-3B
Serial No.	: 853944
Sensitivity (K) 1 CPM	: 0.001 mg/m <sup>3</sup>
Sen. Adjustment Scale Setting	: 685 CPM
Equipment No.	: A-02-04

**Test Conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 59%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Laser Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Laser Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	0.0036
-------------------------	--------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/71213/1
Date of Issue:	2007-12-14
Date Received:	2007-12-13
Date Tested:	2007-12-14
Date Completed:	2007-12-14
Next Due Date:	2008-12-13

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: Integrating Sound Level Meter
Manufacturer	: Brüel & Kjær
Model No.	: B&K 2238
Serial No.	: 2337665
Microphone No.	: 2289749
Equipment No.	: N-01-01

**Test conditions:**

Room Temperature	: 20 degree Celsius
Relative Humidity	: 60%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**  
Senior Chemist

## TEST REPORT

APPLICANT: **Cinotech Consultants Limited**  
**Room 1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, NT, Hong Kong**

Test Report No.:	C/N/80903-2
Date of Issue:	2008-09-03
Date Received:	2008-09-02
Date Tested:	2008-09-02
Date Completed:	2008-09-03
Next Due Date:	2009-09-02

ATTN: **Mr. Henry Leung**

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: Integrating Sound Level Meter
Manufacturer	: Brüel & Kjær
Model No.	: B&K 2238
Serial No.	: 2359303
Equipment No.	: N-01-04

**Test conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 61%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/71116/2
Date of Issue:	2007-11-16
Date Received:	2007-11-15
Date Tested:	2007-11-15
Date Completed:	2007-11-16
Next Due Date:	2008-11-15

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: Brüel & Kjær
Model No.	: 4231
Serial No.	: 2326353
Project No.	: C13
Equipment No.	: N-02-01

### Test conditions:

Room Temperature	: 20 degree Celsius
Relative Humidity	: 59%
Pressure	: 1015.2 hPa

### Methodology:

The sound calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Senior Chemist

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/80903-3
Date of Issue:	2008-09-03
Date Received:	2008-09-02
Date Tested:	2008-09-02
Date Completed:	2008-09-03
Next Due Date:	2009-09-02

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: Brüel & Kjær
Model No.	: 4231
Serial No.	: 2412367
Equipment No.	: N-02-03

### Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 61%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager



## FACTORY CALIBRATION DATA OF THE SVAN 955 nr.: 14302

### 1. CALIBRATION (electrical)

 LEVEL METER; Characteristic: Z;  $f_{sin} = 1000\text{Hz}$ 

Nominal result [dB]	Indication [dB]	Error [dB]
114.0	114.0	0.0

### 2. CALIBRATION\* (acoustical)

LEVEL METER; Range: High; Reference frequency: 1000Hz; Calibration factor: 0.1

Characteristic	Correct value [dB]	Indication [dB]	Error [dB]
Z	113.9	113.8	-0.1
A	113.9	113.8	-0.1
C	113.9	113.8	-0.1

Calibration measured with the microphone ACO type 7052S\_1 No. 35989.

### 3. LINEARITY TEST\* (electrical)

 LEVEL METER; Characteristic: A;  $f_{sin} = 31.5\text{ Hz}$ 

Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Error [dB]	0.0	0.0	-0.1	0.0	-0.1	0.0	-0.1	0.0	0.0	0.0	0.0
Nominal result [dB]	90.0	93.0	94.0	95.0	96.0	97.0	98.0	-	-	-	-
Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-	-	-	-

 LEVEL METER; Characteristic: A;  $f_{sin} = 1000\text{ Hz}$ 

Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Error [dB]	0.0	0.1	0.1	0.1	0.0	0.1	0.0	0.0	0.0	0.0	0.0
Nominal result [dB]	90.0	100.0	110.0	120.0	130.0	133.0	134.0	135.0	136.0	137.0	138.0
Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

 LEVEL METER; Characteristic: A;  $f_{sin} = 8000\text{ Hz}$ 

Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Nominal result [dB]	25.0	26.0	27.0	28.0	29.0	30.0	40.0	50.0	60.0	70.0	80.0
Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
Nominal result [dB]	90.0	100.0	110.0	120.0	130.0	132.0	133.0	134.0	135.0	136.0	137.0
Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

### 4. TONEBURST RESPONSE\* (electrical)

 LEVEL METER; Characteristic: A;  $f_{sin} = 4000\text{ Hz}$ ; Burst duration: 2s;

Steady level nominal result = 135dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2	1	0.5	0.25
MAX	Fast	Indication [dB]	135.0	135.0	134.1	132.5	130.2	126.7	123.9	121.0	117.0	114.0	111.0	107.9
		Error [dB]	0.0	0.1	0.1	0.1	0.0	0.0	0.0	0.1	0.0	0.0	0.0	-0.1
	Slow	Indication [dB]	133.0	130.9	127.5	124.7	121.8	117.9	114.9	111.9	107.9	-	-	-
		Error [dB]	0.0	0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-	-
SEL	-	Indication [dB]	135.0	132.0	128.0	125.0	122.0	118.0	115.0	112.0	108.0	105.0	101.9	98.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1

Steady level nominal result = 115dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2	1	0.5	0.25
MAX	Fast	Indication [dB]	115.0	115.0	114.1	112.4	110.2	106.7	103.9	101.0	97.0	94.0	90.9	87.9
		Error [dB]	0.0	0.1	0.1	0.0	0.0	0.0	0.0	0.1	0.0	0.0	-0.1	-0.1
	Slow	Indication [dB]	113.0	110.9	107.5	104.7	101.8	97.9	94.9	91.9	87.9	-	-	-
		Error [dB]	0.0	0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-	-
SEL	-	Indication [dB]	115.0	112.0	108.0	105.0	102.0	98.0	95.0	92.0	88.0	85.0	81.9	78.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1

Steady level nominal result = 95dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2	1	0.5	0.25
MAX	Fast	Indication [dB]	95.0	94.9	94.0	92.4	90.2	86.7	83.9	80.9	77.0	74.0	70.9	67.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1
	Slow	Indication [dB]	93.0	90.9	87.5	84.7	81.8	77.9	74.9	71.9	67.9	-	-	-
		Error [dB]	0.0	0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-	-
SEL	-	Indication [dB]	95.0	92.0	88.0	85.0	82.0	78.0	75.0	72.0	68.0	65.0	61.9	58.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1

Steady level nominal result = 75dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2	1	0.5	0.25
MAX	Fast	Indication [dB]	75.0	74.9	74.0	72.4	70.2	66.7	63.9	60.9	57.0	54.0	50.9	47.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1
	Slow	Indication [dB]	73.0	70.9	67.5	64.7	61.8	57.9	54.9	51.9	47.9	-	-	-
		Error [dB]	0.0	0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-	-	-
SEL	-	Indication [dB]	75.0	72.0	68.0	65.0	62.0	58.0	55.0	52.0	48.0	45.0	41.9	38.9
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.1	-0.1

Steady level nominal result = 55dB


Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2
MAX	Fast	Indication [dB]	55.0	54.9	54.0	52.4	50.2	46.7	43.9	40.9	37.0
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	Slow	Indication [dB]	53.0	50.9	47.5	44.7	41.8	37.9	34.9	32.0	27.9
		Error [dB]	0.0	0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	0.0
SEL	-	Indication [dB]	55.0	52.0	48.0	45.0	42.0	38.0	35.0	32.0	28.1
		Error [dB]	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

Steady level nominal result = 35dB

Result	Detector	Duration [ms]	1000	500	200
MAX	Fast	Indication [dB]	35.0	34.9	34.0
		Error [dB]	0.0	-0.0	0.0
	Slow	Indication [dB]	32.9	30.9	27.6
		Error [dB]	-0.1	0.0	0.0
SEL	-	Indication [dB]	35.0	32.0	28.0
		Error [dB]	0.0	0.0	0.0

## 5. FREQUENCY RESPONSE\* (electrical)

LEVEL METER; Characteristic: Z; Nominal result (1kHz)=135 dB;



Measured Response (f-frequency, A-attenuation)

f [Hz]	A [dB]	f [Hz]	A [dB]	f [Hz]	A [dB]	f [Hz]	A [dB]
10	3.3	80	0.1	630	0.0	5000	0.1
12.5	2.3	100	0.1	800	0.0	6300	0.1
16	1.6	125	0.1	1000	0.0	8000	0.1
20	1.1	160	0.1	1250	0.0	10000	0.1
25	0.7	200	0.1	1600	0.0	12500	0.0
31.5	0.5	250	0.0	2000	0.0	16000	0.0
40	0.3	315	0.0	2500	0.0	20000	0.1
50	0.2	400	0.0	3150	0.0	-	-
63	0.2	500	0.0	4000	0.1	-	-

All frequencies are nominal center values for the 1/3 octave bands

## 6. INTERNAL NOISE LEVEL\* (electrical - compensated)

LEVEL METER; Backlight - off

Characteristic	Z	A	C
Indication [dB]	10.0	10.0	10.0

\* measured with preamplifier SVANTEK type SV12L No. 17200.

## 7. INTERNAL NOISE LEVEL (acoustical - compensated)

LEVEL METER; Range: LOW; Backlight - off

Characteristic	A
Indication [dB]	<17

Noise measured in special chamber, with reference microphone G.R.A.S type 40AN No. 13529

### ENVIRONMENTAL CONDITIONS

Temperature	Relative humidity	Ambient pressure
24 °C	26 %	1012 hPa

### TEST EQUIPMENT

Item	Manufacturer	Model	Serial no.	Description
1.	SVANTEK	SVAN 401	84	Signal generator
2.	SVANTEK	SVAN 912A	4349	Sound & Vibration Analyser
3.	SOAR	3430	90CA1811	Digital voltmeter
4.	SVANTEK	SV30A	7921	Acoustic calibrator
5.	SVANTEK	ST02	-	Microphone equivalent electrical impedance (18pF)

## CONFORMITY & TEST DECLARATION

1. Herewith SvanTek company declares that this instrument has been calibrated and tested in compliance with the internal ISO9001 procedures and meets all specification given in the Manual(s) or respectively surpass them.
2. The acoustic calibration was performed using the Sound Calibrator and is traceable to the GUM (Central Office of Measures) reference standard - sound level calibrator type 4231 No 2292773.
3. The information appearing on this sheet has been compiled specifically for this instrument. This form is produced with advanced equipment & procedures which permit comprehensive quality assurance verification of all data supplied herein.
4. This calibration sheet shall not be reproduced except in full, without written permission of the SVANTEK Ltd.

Calibration specialist: Anna Domańska

Test date: 2008-01-24

N-09-03

## Sound Calibrator Certificate

Calibrator : Svantek Type SV30A



**Serial no :** 10965  
**Level 1 :** 93.94 dB  
**Level 2 :** 113.94 dB  
**Frequency :** 1000 Hz

### Reference conditions

Pressure : 1013.2 hPa  
Temperature : 23.0 °C  
Relative humidity : 50 %RH

### Masurement conditions

Pressure : 987 hPa  
Temperature : 21 °C  
Relative humidity : 36 %RH

The stated level is valid at reference conditions.

Calibrator signal distortion for 94dB level: 0.08 %  
Calibrator signal distortion for 114dB level: 0.11 %  
Short term level stability : 0.05 dB  
Frequency stability : 0.01 %


Measured according to IEC 60942.

The stated level is relative to 20 uPa .

The level is traceable to GUM, Poland,

with a calculated uncertainty less than  $\pm 0.15$  dB (2 \* sd).

**Date :** 2007-11-09

**Signature :**  .....

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/W/80805-1
Date of Issue:	2008-08-06
Date Received:	2008-08-05
Date Tested:	2008-08-05
Date Completed:	2008-08-06
Next Due Date:	2008-11-05

**ATTN:** Mr. Henry Leung

Page: 1 of 2

### Certificate of Calibration

**Item for calibration:**

Description	: Sonde Environmental Monitoring System
Manufacturer	: YSI
Model No.	: 6820-C-M
Serial No.	: 02D0126AA
Equipment No.	: W.03.01
Project No.	: C013

**Test conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 63%

**Test Specifications:**

Conductivity & Salinity Sensor, Model: 6560, S/N: 05A1209  
1. Conductivity performance check with Potassium Chloride standard solution  
2. Salinity performance check with Sodium Chloride standard solution  
Dissolved Oxygen Sensor, Model: 6562, S/N: 04A0145  
1. Performance check against Winkler titration  
Turbidity Sensor, Model: 6136, S/N: 05A1610AJ  
1. Calibration check with Formazin standard solution  
pH Meter, Model: 6561, S/N: 01J  
1. Calibration check with standard pH buffer  
Depth Meter  
1. Calibration check at 1m water level depth

**Methodologies:**

1. YSI 6-Series Sonde Environmental Monitoring System Instruction Manual
2. In-house method with reference to APHA and ISO standards

*PREPARED AND CHECKED BY:*  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

**TEST REPORT**

Test Report No.:	C/W/80805-1
Date of Issue:	2008-08-06
Date Received:	2008-08-05
Date Tested:	2008-08-05
Date Completed:	2008-08-06
Next Due Date:	2008-11-05

Page: 2 of 2

**Results:**

1. Conductivity performance check

Specific Conductivity, $\mu\text{S}/\text{cm}$		Correction, $\mu\text{S}/\text{cm}$	Acceptable range
Salinity Meter (C1)	Theoretical Value (C2)	$D = C1 - C2$	
1421	1420	2	$1420 \pm 20$

2. Salinity Performance check

Salinity, ppt		Correction, ppt	Acceptable range
Instrument Reading	Theoretical Value		
30.0	30.0	0.0	$30.0 \pm 3$

3. Dissolved Oxygen check

Oxygen level in water at 20°C	Dissolved Oxygen, mg O <sub>2</sub> /L		Correction, mg O <sub>2</sub> /L	Acceptable range
	D.O. Meter	Winkler Titration		
Saturated	9.1	9.1	0.0	$\pm 0.2$
Half-saturated	5.6	5.6	0.0	$\pm 0.2$
Zero	0.0	0.0	0.0	$\pm 0.2$

4. Turbidity check

Turbidity value in solution, NTU	Calibration Value, NTU	Correction, NTU	Acceptable range
0.00	0.00	0.00	$0.00 \pm 0.05$
100	100	0	$100 \pm 5$

5. pH Meter check

Test Parameters	Performance characteristic	Acceptable range
Liquid junction error $\Delta\text{pH}_l$ , pH unit	0.01	Less than 0.05
Shift on stirring $\Delta\text{pH}_s$ , pH unit	0.01	Less than 0.02
Noise $\Delta\text{pH}_n$ , pH unit	0.00	Less than 0.02

6. Depth Meter check

Instrument Reading, m	Calibration Value, m	Correction, m	Acceptable range
1.0	1.00	0.00	$1.00 \pm 0.05$

\*\*\*\*\*END OF REPORT\*\*\*\*\*

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/W/80805-2
Date of Issue:	2008-08-06
Date Received:	2008-08-05
Date Tested:	2008-08-05
Date Completed:	2008-08-06
Next Due Date:	2008-11-05

**ATTN:** Mr. Henry Leung

Page: 1 of 2

### Certificate of Calibration

**Item for calibration:**

Description	: Sonde Environmental Monitoring System
Manufacturer	: YSI
Model No.	: 6820-C-M
Serial No.	: 02D0293AA
Equipment No.	: W.03.02
Project No.	: C013

**Test conditions:**

Room Temperature	: 23 degree Celsius
Relative Humidity	: 63%

**Test Specifications:**

Conductivity & Salinity Sensor, Model: 6560, S/N: 02C0886

1. Conductivity performance check with Potassium Chloride standard solution
2. Salinity performance check with Sodium Chloride standard solution

Dissolved Oxygen Sensor, Model: 6562, S/N: 0261137

1. Performance check against Winkler titration

Turbidity Sensor, Model: 6136, S/N: 05F2030AQ

1. Calibration check with Formazin standard solution

pH Meter, Model: 6561, S/N: 02A

1. Calibration check with standard pH buffer

Depth Meter

1. Calibration check at 1m water level depth

**Methodologies:**

1. YSI 6-Series Sonde Environmental Monitoring System Instruction Manual
2. In-house method with reference to APHA and ISO standards

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

Test Report No.:	C/W/80805-2
Date of Issue:	2008-08-06
Date Received:	2008-08-05
Date Tested:	2008-08-05
Date Completed:	2008-08-06
Next Due Date:	2008-11-05

Page: 2 of 2

### Results:

#### 1. Conductivity performance check

Specific Conductivity, $\mu\text{S}/\text{cm}$		Correction, $\mu\text{S}/\text{cm}$	Acceptable range
Salinity Meter (C1)	Theoretical Value (C2)	$D = C1 - C2$	
1420	1420	0	$1420 \pm 20$

#### 2. Salinity Performance check

Salinity, ppt		Correction, ppt	Acceptable range
Instrument Reading	Theoretical Value		
30.1	30.0	0.1	$30.0 \pm 3$

#### 3. Dissolved Oxygen check

Oxygen level in water at 20°C	Dissolved Oxygen, mg O <sub>2</sub> /L		Correction, mg O <sub>2</sub> /L	Acceptable range
	D.O. Meter	Winkler Titration		
Saturated	9.0	9.0	0.0	$\pm 0.2$
Half-saturated	5.8	5.8	0.0	$\pm 0.2$
Zero	0.0	0.0	0.0	$\pm 0.2$

#### 4. Turbidity check

Turbidity value in solution, NTU	Calibration Value, NTU	Correction, NTU	Acceptable range
0.00	0.00	0.00	$0.00 \pm 0.05$
100	100	0	$100 \pm 5$

#### 5. pH Meter check

Test Parameters	Performance characteristic	Acceptable range
Liquid junction error $\Delta\text{pH}_l$ , pH unit	0.01	Less than 0.05
Shift on stirring $\Delta\text{pH}_s$ , pH unit	0.01	Less than 0.02
Noise $\Delta\text{pH}_n$ , pH unit	0.01	Less than 0.02

#### 6. Depth Meter check

Instrument Reading, m	Calibration Value, m	Correction, m	Acceptable range
1.0	1.00	0.00	$1.00 \pm 0.05$

\*\*\*\*\*END OF REPORT\*\*\*\*\*

---

---

**APPENDIX C  
QUALITY CONTROL REPORTS FOR SS  
LABORATORY ANALYSIS**

---

---



**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07382
Date of Issue:	2008/10/03
Date Received:	2008/10/02
Date Tested:	2008/10/02
Date Completed:	2008/10/03

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/02  
Number of Sample: 58  
Custody No.: MA8001/81002

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake B bf	15	16	8	96

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07405
Date of Issue:	2008/10/08
Date Received:	2008/10/04
Date Tested:	2008/10/04
Date Completed:	2008/10/08

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/04  
Number of Sample: 58  
Custody No.: MA8001/81004

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
I2 bf	12	14	14	102

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07406
Date of Issue:	2008/10/08
Date Received:	2008/10/06
Date Tested:	2008/10/06
Date Completed:	2008/10/08

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/06  
Number of Sample: 58  
Custody No.: MA8001/81006

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
I2be	12	13	6	100

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07416
Date of Issue:	2008/10/09
Date Received:	2008/10/08
Date Tested:	2008/10/08
Date Completed:	2008/10/09

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/08  
Number of Sample: 30  
Custody No.: MA8001/81008

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake B be	13	15	13	105

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07431
Date of Issue:	2008/10/13
Date Received:	2008/10/10
Date Tested:	2008/10/10
Date Completed:	2008/10/13

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/10  
Number of Sample: 58  
Custody No.: MA8001/81010

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	15	17	8	97

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07443
Date of Issue:	2008/10/14
Date Received:	2008/10/13
Date Tested:	2008/10/13
Date Completed:	2008/10/14

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/13  
Number of Sample: 58  
Custody No.: MA8001/81013

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	8	7	13	99

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07457
Date of Issue:	2008/10/16
Date Received:	2008/10/15
Date Tested:	2008/10/15
Date Completed:	2008/10/16

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/15  
Number of Sample: 58  
Custody No.: MA8001/81015

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	12	12	3	95

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07477
Date of Issue:	2008/10/20
Date Received:	2008/10/17
Date Tested:	2008/10/17
Date Completed:	2008/10/20

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/17  
Number of Sample: 58  
Custody No.: MA8001/81017

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	8	10	17	104

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*



**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07485
Date of Issue:	2008/10/21
Date Received:	2008/10/20
Date Tested:	2008/10/20
Date Completed:	2008/10/21

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/20  
Number of Sample: 58  
Custody No.: MA8001/81020

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
12 mf	11	12	9	94

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07499
Date of Issue:	2008/10/23
Date Received:	2008/10/22
Date Tested:	2008/10/22
Date Completed:	2008/10/23

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/22  
Number of Sample: 30  
Custody No.: MA8001/81022

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	6	6	12	94

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07515
Date of Issue:	2008/10/27
Date Received:	2008/10/24
Date Tested:	2008/10/24
Date Completed:	2008/10/27

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/24  
Number of Sample: 58  
Custody No.: MA8001/81024

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	11	12	15	94

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07520
Date of Issue:	2008/10/28
Date Received:	2008/10/27
Date Tested:	2008/10/27
Date Completed:	2008/10/28

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/27  
Number of Sample: 58  
Custody No.: MA8001/81027

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	12	11	11	94

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07533
Date of Issue:	2008/10/30
Date Received:	2008/10/29
Date Tested:	2008/10/29
Date Completed:	2008/10/30

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/29  
Number of Sample: 58  
Custody No.: MA8001/81029

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	16	17	7	91

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

**TEST REPORT**  
**QC REPORT**

**APPLICANT: Cinotech Consultants Limited**  
**Rm1710, Technology Park,**  
**18 On Lai Street,**  
**Shatin, N.T.**

Laboratory No.:	07553
Date of Issue:	2008/11/03
Date Received:	2008/10/31
Date Tested:	2008/10/31
Date Completed:	2008/11/03

**ATTN: Mr. Henry Leung**

Page: 1 of 1

Sampling Site: Design and Construction of Hong Kong West Drainage Tunnel  
Project No.: MA8001  
Sampling Date: 2008/10/31  
Number of Sample: 58  
Custody No.: MA8001/81031

\*\*\*\*\*

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
Intake A se	12	14	13	97

\*\*\*\*\*END OF REPORT\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

*Laboratory Manager*

---

---

**APPENDIX D  
ENVIRONMENTAL MONITORING  
SCHEDULES**

---

---

**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Impact Air and Noise Monitoring Schedule for October 2008 (Eastern Portal)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	29-Sep	30-Sep	<b>1-Oct</b>	2-Oct	3-Oct	4-Oct
	1 hr TSP	1 hr TSP			1 hr TSP Noise	
<b>5-Oct</b>	6-Oct	<b>7-Oct</b>	8-Oct	9-Oct	10-Oct	11-Oct
	1 hr TSP		24 hrs TSP	1 hr TSP Noise 24 hrs TSP	1 hr TSP	
<b>12-Oct</b>	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct
		1 hr TSP Noise	1 hr TSP 24 hrs TSP	1 hr TSP		
<b>19-Oct</b>	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
		1 hr TSP 24 hrs TSP	1 hr TSP	1 hr TSP Noise		
<b>26-Oct</b>	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
	24 hrs TSP	1 hr TSP	1 hr TSP		1 hr TSP Noise Day Time (07:00-19:00) & *Evening Time (19:00-23:00)	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AQ1 - True Light Middle School of HK

**Noise Monitoring Station**

NC1 - True Light Middle School of HK

NC2 - The Legend (\*)



**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Impact Air and Noise Monitoring Schedule for October 2008 (Western Portal)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	29-Sep	30-Sep	1-Oct	2-Oct	3-Oct	4-Oct
	1 hr TSP	1 hr TSP			1 hr TSP Noise 24 hrs TSP	
5-Oct	6-Oct	7-Oct	8-Oct	9-Oct	10-Oct	11-Oct
	1 hr TSP			1 hr TSP Noise 24 hrs TSP	1 hr TSP	
12-Oct	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct
		1 hr TSP Noise	1 hr TSP 24 hrs TSP	1 hr TSP		
19-Oct	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
<u>NOISE</u> Day Time (07:00-19:00)		1 hr TSP 24 hrs TSP	1 hr TSP	1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)		
26-Oct	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
<u>NOISE</u> Day Time (07:00-19:00)	24 hrs TSP	1 hr TSP	1 hr TSP		1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AQ2 - Outside Aegean Terrace (1 hour TSP)  
AQ3 - Outside Site Office at Western Portal (24 hours TSP)

**Noise Monitoring Station**

NC3 - Outside Aegean Terrace

**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Impact Water Quality Monitoring Schedule for October 2008**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
<b>28-Sep</b>	29-Sep	30-Sep	<b>1-Oct</b>	2-Oct	3-Oct	4-Oct
				Mid-Flood 8:05 Mid-Ebb 13:57		Mid-Flood 9:32 Mid-Ebb 14:52
<b>5-Oct</b>	6-Oct	<b>7-Oct</b>	8-Oct	9-Oct	10-Oct	11-Oct
	Mid-Flood 8:00 Mid-Ebb 17:00		Mid-Ebb 8:00 Mid-Flood N/A		Mid-Ebb 8:52 Mid-Flood 16:39	
<b>12-Oct</b>	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct
	Mid-Ebb 11:04 Mid-Flood 17:24		Mid-Ebb 12:26 Mid-Flood 18:00		Mid-Flood 8:08 Mid-Ebb 13:48	
<b>19-Oct</b>	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
	Mid-Flood 11:35 Mid-Ebb 16:02		Mid-Ebb 8:00 Mid-Flood N/A		Mid-Ebb 8:49 Mid-Flood 15:53	
<b>26-Oct</b>	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
	Mid-Ebb 11:16 Mid-Flood 17:09		Mid-Ebb 12:26 Mid-Flood 17:51		Mid-Flood 8:00 Mid-Ebb 13:27	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

NA indicated favourable tide occurs during non-working hours

**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Tentative Impact Air and Noise Monitoring Schedule for November 2008 (Eastern Portal)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
<b>26-Oct</b>	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
						24 hrs TSP
<b>2-Nov</b>	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov
	1 hr TSP	1 hr TSP		1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)	24 hrs TSP	
<b>9-Nov</b>	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov
	1 hr TSP	1 hr TSP		24 hrs TSP	1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)	
<b>16-Nov</b>	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov
		1 hr TSP	1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00) 24 hrs TSP	1 hr TSP		
<b>23-Nov</b>	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov
		1 hr TSP  24 hrs TSP	1 hr TSP	1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)		
<b>30-Nov</b>	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec
	24 hrs TSP	1 hr TSP	1 hr TSP <u>Noise</u> Day Time (07:00-19:00) & Evening Time (19:00-23:00)		1 hr TSP	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AQ1 - True Light Middle School of HK

**Noise Monitoring Station**

NC1 - True Light Middle School of HK  
NC2 - The Legend

**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Tentative Impact Air and Noise Monitoring Schedule for November 2008 (Western Portal)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
<b>26-Oct</b>	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
						24 hrs TSP
<b>2-Nov</b>	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov
<u>1</u> NOISE Day Time (07:00-19:00)	1 hr TSP	1 hr TSP		1 hr TSP Noise Day Time (07:00-19:00) & Evening Time (19:00-23:00)	24 hrs TSP	
<b>9-Nov</b>	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov
<u>1</u> NOISE Day Time (07:00-19:00)	1 hr TSP	1 hr TSP		24 hrs TSP	1 hr TSP Noise Day Time (07:00-19:00) & Evening Time (19:00-23:00)	
<b>16-Nov</b>	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov
<u>1</u> NOISE Day Time (07:00-19:00)		1 hr TSP	1 hr TSP Noise Day Time (07:00-19:00) & Evening Time (19:00-23:00) 24 hrs TSP	1 hr TSP		
<b>23-Nov</b>	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov
<u>1</u> NOISE Day Time (07:00-19:00)		1 hr TSP 24 hrs TSP	1 hr TSP	1 hr TSP Noise Day Time (07:00-19:00) & Evening Time (19:00-23:00)		
<b>30-Nov</b>	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec
<u>1</u> NOISE Day Time (07:00-19:00)	24 hrs TSP	1 hr TSP	1 hr TSP Noise Day Time (07:00-19:00) & Evening Time (19:00-23:00)		1 hr TSP	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AQ2 - Outside Aegean Terrace (1 hour TSP)  
AQ3 - Outside Site Office at Western Portal (24 hours TSP)

**Noise Monitoring Station**

NC3 - Outside Aegean Terrace

**Drainage Improvement in Northern Hong Kong Island - Hong Kong West Drainage Tunnel  
Tentative Impact Water Quality Monitoring Schedule for November 2008**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
26-Oct	27-Oct	28-Oct	29-Oct	30-Oct	31-Oct	1-Nov
	Mid-Ebb 11:16 Mid-Flood 17:09		Mid-Ebb 12:26 Mid-Flood 17:51		Mid-Flood 8:00 Mid-Ebb 13:27	
2-Nov	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov
	Mid-Flood 10:39 Mid-Ebb 15:14		Mid-Flood 16:00 Mid-Ebb N/A		Mid-Ebb 8:00 Mid-Flood 14:46	
9-Nov	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov
	Mid-Ebb 9:32 Mid-Flood 15:55		Mid-Ebb 11:11 Mid-Flood 16:46		Mid-Ebb 12:43 Mid-Flood 17:43	
16-Nov	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov
	Mid-Flood 10:18 Mid-Ebb 15:09		Mid-Flood 12:32 Mid-Ebb 17:33		Mid-Ebb 8:00 Mid-Flood 14:11	
23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov
	Mid-Ebb 9:57 Mid-Flood 15:49		Mid-Ebb 11:23 Mid-Flood 16:30		Mid-Ebb 12:29 Mid-Flood 17:10	

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)  
NA indicated favourable tide occurs during non-working hours

---

---

**APPENDIX E  
1-HOUR TSP MONITORING RESULTS  
AND GRAPHICAL PRESENTATION**

---

---

## Appendix E - 1-hour TSP Monitoring Results

### Station AQ1 (True Light Middle School of Hong Kong)



Date	Sampling Time	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
					Initial	Final		Initial	Final		Initial	Final			
3-Oct-08	09:00	Cloudy	299.5	761.5	2.8442	2.8578	0.0136	2013.3	2014.3	1.0	1.23	1.23	1.23	73.7	184.5
6-Oct-08	14:00	Cloudy	298.3	759.7	2.8914	2.9125	0.0211	2021.3	2022.3	1.0	1.23	1.23	1.23	73.8	286.0
9-Oct-08	15:00	Cloudy	301.5	763.7	2.8532	2.8593	0.0061	2046.3	2047.3	1.0	1.23	1.23	1.23	73.6	82.9
10-Oct-08	16:00	Sunny	302.9	763.1	2.9014	2.9071	0.0057	2071.3	2072.3	1.0	1.22	1.22	1.22	73.4	77.6
14-Oct-08	09:00	Cloudy	298.3	765.9	2.8866	2.9019	0.0153	2072.3	2073.3	1.0	1.23	1.23	1.23	74.0	206.6
15-Oct-08	09:00	Cloudy	299.3	765.4	2.8149	2.8266	0.0117	2073.3	2074.3	1.0	1.22	1.22	1.22	73.2	159.8
16-Oct-08	14:15	Sunny	302.9	761.3	2.7956	2.8118	0.0162	2098.3	2099.3	1.0	1.21	1.21	1.21	72.7	223.0
21-Oct-08	09:00	Sunny	299.6	764.5	2.8318	2.8558	0.0240	2099.3	2100.3	1.0	1.22	1.22	1.22	73.2	328.1
22-Oct-08	15:00	Sunny	301.8	761.3	2.8129	2.8206	0.0077	2124.3	2125.3	1.0	1.21	1.21	1.21	72.8	105.8
23-Oct-08	09:00	Sunny	299.9	763.8	2.8496	2.8659	0.0163	2125.3	2126.3	1.0	1.22	1.22	1.22	73.1	223.0
28-Oct-08	10:40	Sunny	299.1	766.5	2.8530	2.8643	0.0113	2150.3	2151.3	1.0	1.22	1.22	1.22	73.3	154.2
29-Oct-08	09:00	Sunny	299.9	764.5	2.8685	2.8859	0.0174	2151.3	2152.3	1.0	1.22	1.22	1.22	73.1	238.0
31-Oct-08	09:00	Sunny	300.0	765.2	2.8651	2.8821	0.0170	2152.3	2153.3	1.0	1.22	1.22	1.22	73.1	232.4
														Min	77.6
														Max	328.1
														Average	192.4

## Appendix E - 1-hour TSP Monitoring Results

Station AQ2 (Outside Aegean Terrace)			
Date	Time	Weather	Particulate Concentration ( $\mu\text{g}/\text{m}^3$ )
3-Oct-08	15:05	Cloudy	32.9
6-Oct-08	15:15	Cloudy	35.3
9-Oct-08	15:00	Cloudy	37.2
10-Oct-08	16:00	Sunny	37.2
14-Oct-08	11:00	Cloudy	49.5
15-Oct-08	15:10	Cloudy	48.3
16-Oct-08	16:00	Sunny	52.9
21-Oct-08	15:00	Sunny	37.5
22-Oct-08	15:25	Sunny	50.4
23-Oct-08	15:30	Sunny	46.3
28-Oct-08	13:00	Sunny	51.2
29-Oct-08	16:15	Sunny	53.1
31-Oct-08	13:00	Sunny	46.7
		Average	44.5
		Maximum	53.1
		Minimum	32.9



### 1-hr TSP Concentration Levels

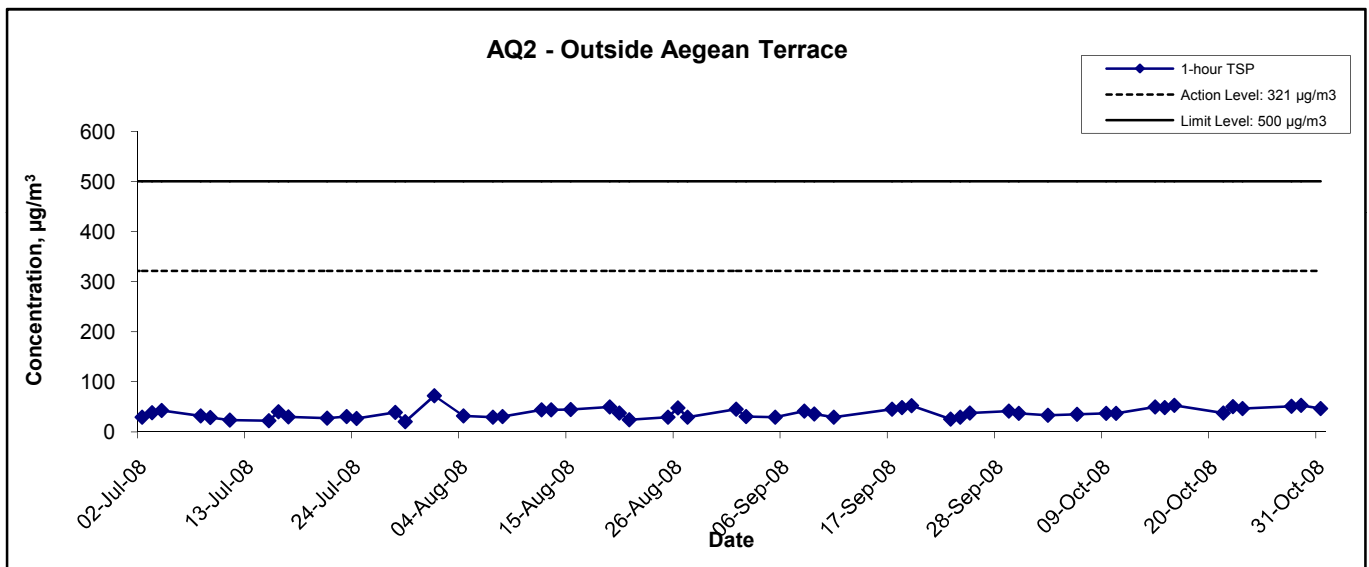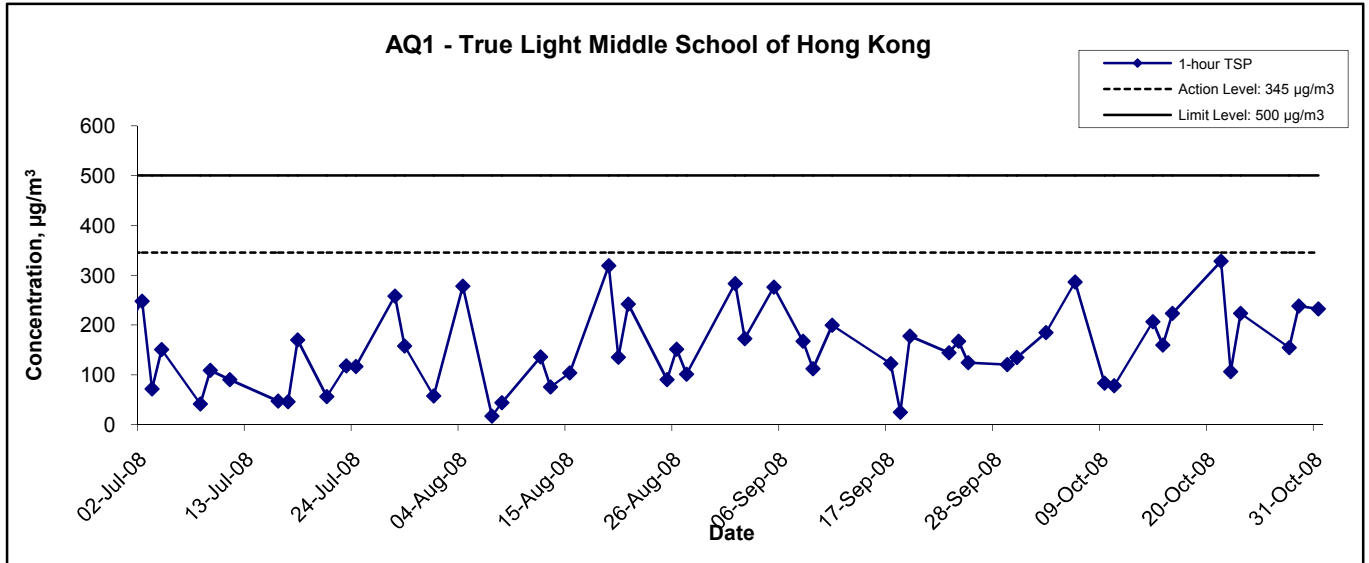

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of 1-hour TSP Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix E	

---

---

**APPENDIX F  
24-HOUR TSP MONITORING RESULTS  
AND GRAPHICAL PRESENTATION**

---

---

## Appendix F - 24-hour TSP Monitoring Results



### Station AQ1 - True Light Middle School of Hong Kong

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
8-Oct-08	Cloudy	300.1	762.4	2.8924	3.0576	0.1652	2022.3	2046.3	24.0	1.23	1.23	1.23	1768.8	93.4
9-Oct-08	Sunny	301.2	763.2	2.9214	3.0362	0.1148	2047.3	2071.3	24.0	1.23	1.23	1.23	1766.7	65.0
15-Oct-08	Sunny	302.1	763.9	2.8767	3.0516	0.1749	2074.3	2098.3	24.0	1.21	1.21	1.21	1748.5	100.0
21-Oct-08	Sunny	299.8	764.1	2.8197	2.9765	0.1568	2100.3	2124.3	24.0	1.22	1.22	1.22	1754.8	89.4
27-Oct-08	Sunny	299.9	767.1	2.8712	3.1109	0.2397	2126.3	2150.3	24.0	1.22	1.22	1.22	1757.6	136.4
													Min	65.0
													Max	136.4
													Average	96.8

### Station AQ3 - Outside Site Office (Western Portal)

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure (Pa)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )
				Initial	Final		Initial	Final		Initial	Final			
3-Oct-08	Cloudy	299.5	761.5	2.8518	3.0059	0.1541	6203.2	6227.2	24.0	1.22	1.22	1.22	1762.4	87.4
9-Oct-08	Sunny	300.3	765.3	2.8649	2.9854	0.1205	6227.2	6251.2	24.0	1.23	1.23	1.23	1764.4	68.3
15-Oct-08	Sunny	299.3	765.4	2.8507	3.0192	0.1685	6251.2	6275.2	24.0	1.22	1.22	1.22	1760.5	95.7
21-Oct-08	Sunny	299.6	764.5	2.8177	2.8658	0.0481	6275.2	6299.2	24.0	1.22	1.22	1.22	1758.7	27.4
27-Oct-08	Sunny	299.9	767.1	2.8391	2.9483	0.1092	6299.2	6323.2	24.0	1.22	1.22	1.22	1760.6	62.0
													Min	27.4
													Max	95.7
													Average	68.2

## 24-hr TSP Concentration Levels

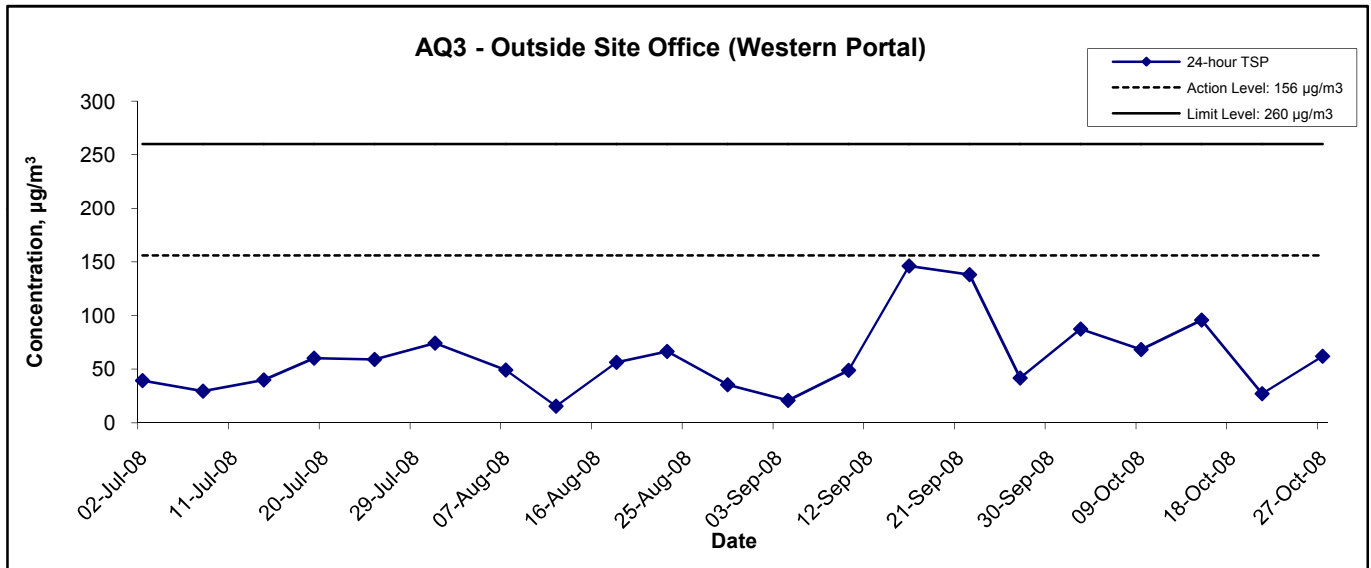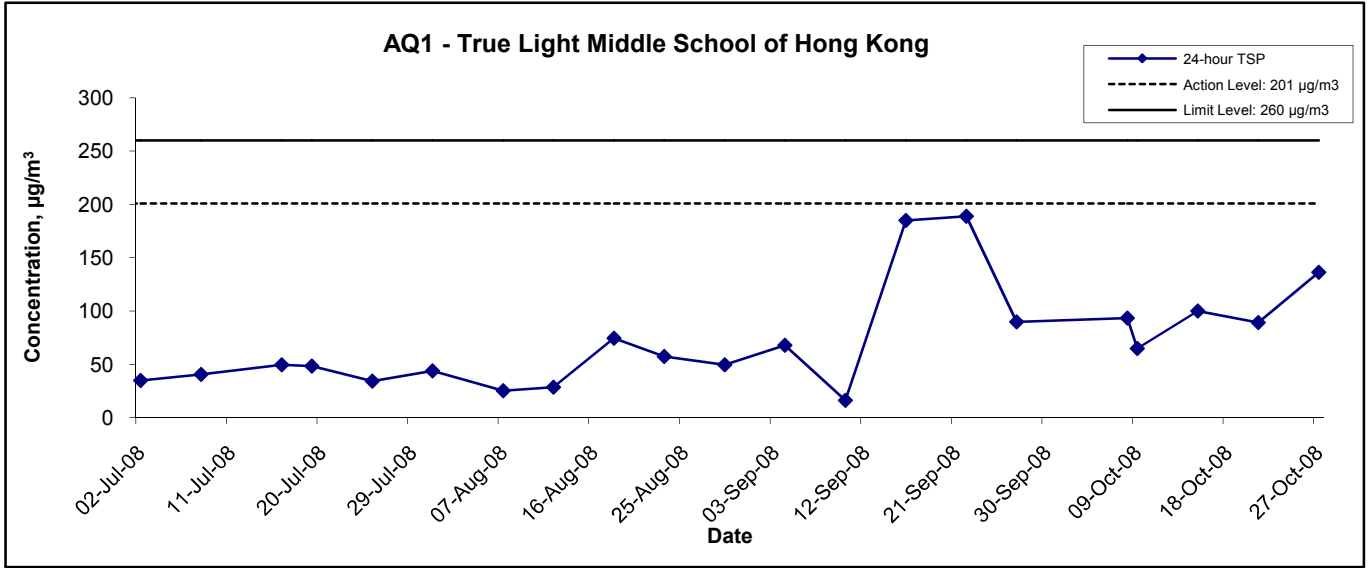

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of 24-hour TSP Monitoring Results	Scale	N.T.S	Project No.	MA8001	CINOTECH
	Date	Oct 08	Appendix	F	

---

---

**APPENDIX G  
NOISE MONITORING RESULTS AND  
GRAPHICAL PRESENTATION**

---

---

## Appendix G - Noise Monitoring Results

Location NC1 - True Light Middle School of Hong Kong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
3-Oct-08	13:00	Cloudy	67.8	69.0	65.5	70.2	67.8, Measured ≤ Baseline
9-Oct-08	13:00	Cloudy	67.8	69.5	66.0		67.8, Measured ≤ Baseline
14-Oct-08	13:00	Cloudy	64.2	66.5	61.5		64.2, Measured ≤ Baseline
23-Oct-08	14:00	Sunny	68.7	70.5	65.5		68.7, Measured ≤ Baseline
31-Oct-08	10:00	Sunny	68.2	69.5	66.5		68.2, Measured ≤ Baseline

Location NC2 - The Legend							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
3-Oct-08	13:45	Cloudy	65.1	66.5	64.0	64.8	53.3
9-Oct-08	13:40	Cloudy	66.1	68.5	65.0		60.2
14-Oct-08	13:40	Cloudy	62.8	64.5	59.0		62.8, Measured ≤ Baseline
23-Oct-08	14:40	Sunny	69.2	71.5	66.0		67.2
31-Oct-08	10:45	Sunny	67.1	69.5	64.5		63.2

Location NC3 - Outside Aegean Terrace							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
3-Oct-08	15:05	Cloudy	59.3	61.0	57.0	57.7	54.2
9-Oct-08	15:05	Cloudy	60.2	61.5	56.5		56.6
14-Oct-08	11:00	Cloudy	58.3	60.0	53.5		49.4
23-Oct-08	15:30	Sunny	60.3	62.0	55.5		56.8
31-Oct-08	13:00	Sunny	60.3	61.5	57.5		56.8

**Appendix G - Noise Monitoring Results**




(Restricted Hours - 19:00 to 23:00 on normal weekdays )

Location NC2 - The Legend								
Date	Time	Weather	dB (A) (5-min)				Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	Average L <sub>eq</sub>	L <sub>eq</sub>	L <sub>eq</sub>
31-Oct-08	19:45	Fine	59.3	61.5	56.0	59.5	59.1	48.9
	19:50		59.5	62.0	56.0			
	19:55		59.8	62.5	56.5			

(Restricted Hours - 07:00 - 23:00 hrs holidays & 19:00 - 23:00 hrs on all other days )

Location NC3 - Outside Aegean Terrace								
Date	Time	Weather	dB (A) (5-min)				Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	Average L <sub>eq</sub>	L <sub>eq</sub>	L <sub>eq</sub>
19-Oct-08	13:00	Fine	58.6	60.7	53.1	58.6	53.8	56.9
	13:05		58.4	61.0	53.2			
	13:10		58.8	61.0	53.5			
23-Oct-08	19:10	Fine	49.2	50.8	46.3	50.6	53.8	50.6, Measured ≤ Baseline
	19:15		50.6	51.5	46.8			
	19:20		51.7	53.8	48.5			
26-Oct-08	13:30	Sunny	57.6	60.5	54.0	58.0	53.8	55.9
	13:35		58.1	61.5	54.0			
	13:40		58.2	61.5	54.0			
31-Oct-08	20:30	Fine	50.2	52.0	47.0	50.4	53.8	50.4, Measured ≤ Baseline
	20:35		50.4	52.0	46.5			
	20:40		50.5	52.0	47.0			


## Noise Levels

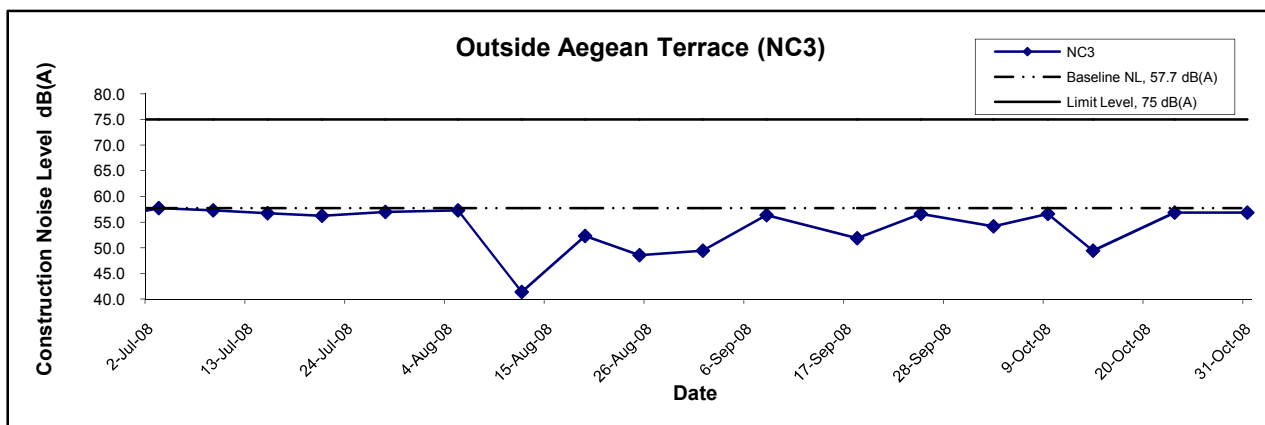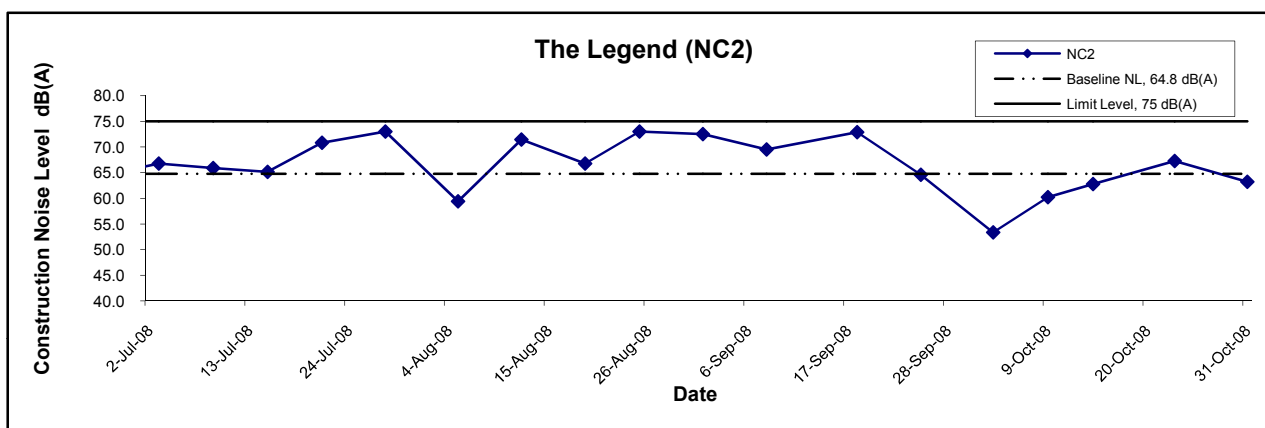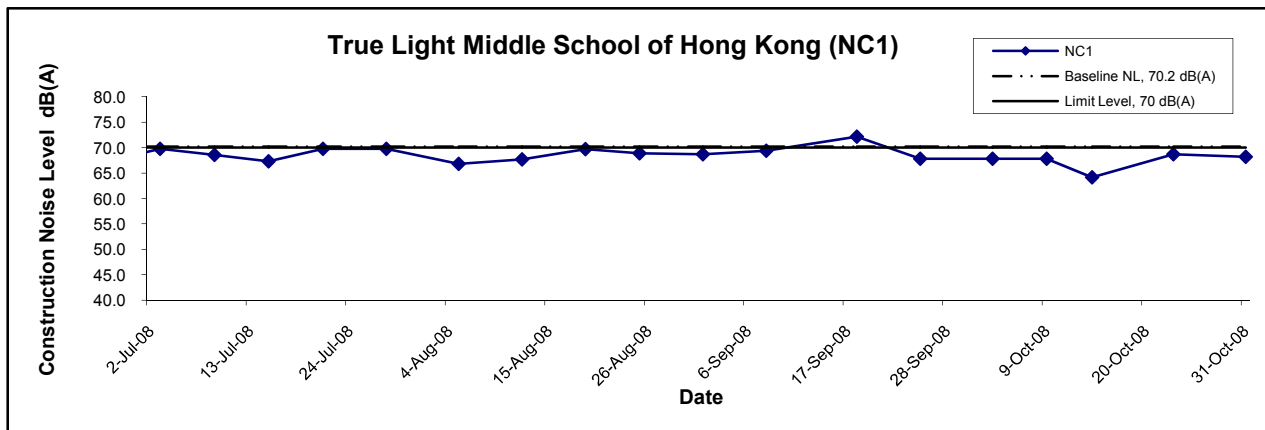


Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix G	



**Noise Levels  
(Restricted Hours - 19:00 to 23:00 on normal weekdays )**

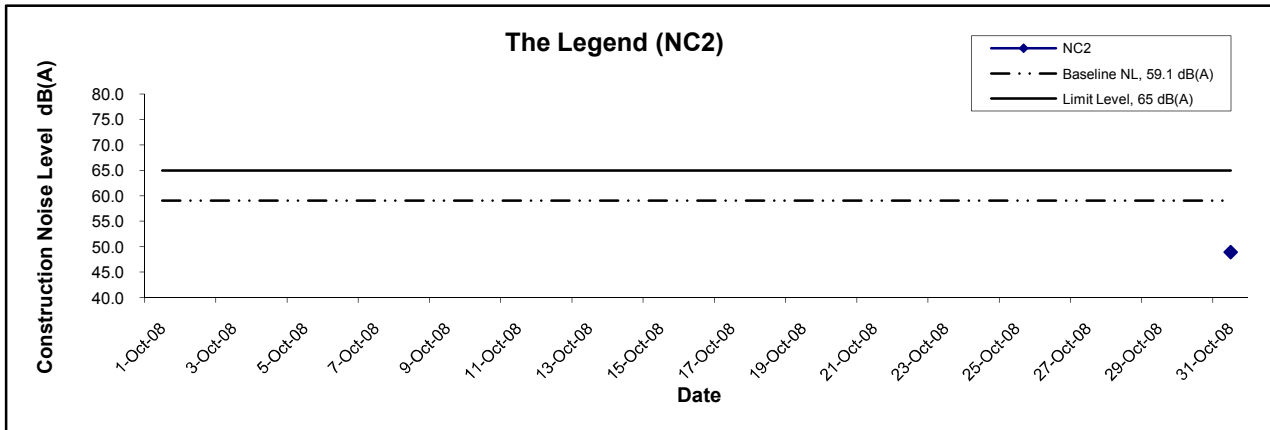

**Noise Levels  
(Restricted Hours - 07:00 - 23:00 hrs holidays & 19:00 - 23:00 hrs on all other days )**

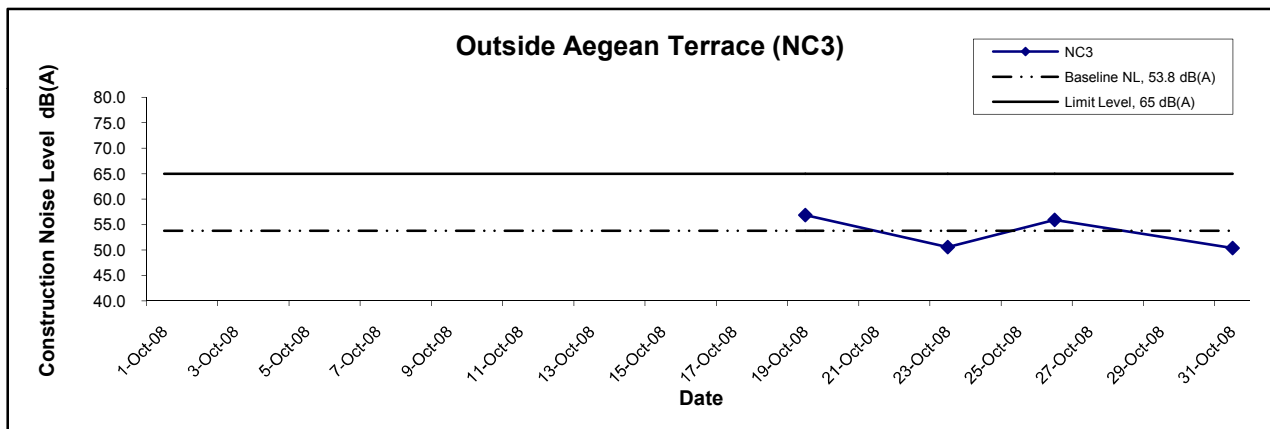

Title	Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel	Scale	Project No.	<b>CINOTECH</b>
	Graphical Presentation of Construction Noise Monitoring Results	N.T.S	MA8001	
		Date	Appendix	
		Oct 08	G	

---

---

**APPENDIX H  
WATER QUALITY MONITORING  
RESULTS AND GRAPHICAL  
PRESENTATION**

---

---

### Water Quality Monitoring Results at CE - Mid-Ebb Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	14:31	Surface	1	27.1 27.5	27.3	8.2 7.3	7.8	28.2 28.0	28.1	91.4 91.4	91.4	6.7 6.7	6.7	7.0	3.0 3.0	3.0	3.7	6.0 6.0	6.0	8.7
				Middle	5.5	26.8 26.6	26.7	8.8 8.9	8.9	28.8 29.0	28.9	102.0 98.4	100.2	7.2 7.1	7.2		3.5 3.9	3.7		11.0 11.0	11.0	
				Bottom	10	26.1 26.1	26.1	7.5 8.5	8.0	29.4 29.2	29.3	73.6 72.9	73.3	6.1 6.0	6.1		4.5 4.5	4.5		4.5 4.5	4.5	
4-Oct-08	Cloudy	Calm	15:26	Surface	1	27.2 27.5	27.4	8.3 7.4	7.9	28.3 28.0	28.2	91.4 91.4	91.4	6.7 6.7	6.7	7.0	2.9 2.9	2.9	3.7	8.0 8.0	8.0	9.0
				Middle	5.5	26.8 26.7	26.8	8.7 8.7	8.7	28.8 28.8	28.8	102.0 98.2	100.1	7.3 7.1	7.2		3.6 3.9	3.8		8.0 8.0	8.0	
				Bottom	10	26.2 25.9	26.1	7.6 8.5	8.1	29.3 29.3	29.3	80.5 79.8	80.2	6.5 6.3	6.4		4.5 4.3	4.4		4.5 4.3	4.4	
6-Oct-08	Cloudy	Calm	17:16	Surface	1	25.7 25.7	25.7	7.6 7.6	7.6	28.7 28.7	28.7	92.7 92.1	92.4	7.0 7.0	7.0	6.9	1.7 1.6	1.7	2.1	8.0 8.0	8.0	9.7
				Middle	5.5	24.8 24.8	24.8	8.2 8.3	8.3	30.8 30.9	30.9	88.6 88.0	88.3	6.8 6.7	6.8		1.8 1.9	1.9		8.0 8.0	8.0	
				Bottom	10	25.5 25.5	25.5	7.0 7.8	7.4	30.2 30.6	30.4	88.1 84.1	86.1	6.7 6.5	6.6		2.8 2.8	2.8		13.0 13.0	13.0	
8-Oct-08	Sunny	Calm	09:23	Surface	1	25.8 25.8	25.8	8.3 8.3	8.3	29.5 29.5	29.5	93.4 92.6	93.0	6.7 6.6	6.7	6.4	1.8 1.7	1.8	2.3	8.0 8.0	8.0	11.3
				Middle	6	25.3 25.2	25.3	8.5 8.6	8.6	30.5 30.4	30.5	87.3 86.4	86.9	6.0 6.1	6.1		2.1 2.1	2.1		10.0 10.0	10.0	
				Bottom	11	25.1 25.0	25.1	7.9 8.4	8.2	31.1 31.1	31.1	82.7 84.3	83.5	6.2 6.2	6.2		2.9 2.9	2.9		16.0 16.0	16.0	
10-Oct-08	Sunny	Calm	10:01	Surface	1	26.7 26.7	26.7	8.0 8.1	8.1	29.5 29.9	29.7	86.4 87.0	86.7	6.5 6.5	6.5	6.4	2.3 2.3	2.3	2.6	12.0 12.0	12.0	12.3
				Middle	5.5	26.5 26.5	26.5	8.7 8.6	8.7	29.9 30.2	30.1	82.6 82.4	82.5	6.3 6.3	6.3		2.6 2.5	2.6		10.0 10.0	10.0	
				Bottom	10	26.0 26.0	26.0	7.8 8.1	8.0	30.2 29.4	29.8	81.4 82.1	81.8	6.2 6.2	6.2		2.9 3.1	3.0		15.0 15.0	15.0	
13-Oct-08	Sunny	Calm	11:55	Surface	1	26.8 26.8	26.8	7.2 7.5	7.4	32.0 32.0	32.0	93.3 91.3	92.3	6.9 6.8	6.9	6.9	4.3 4.3	4.3	5.3	13.0 13.0	13.0	10.5
				Middle	5.5	26.8 26.8	26.8	7.9 7.3	7.6	31.7 31.8	31.8	90.8 90.8	90.8	6.8 6.8	6.8		5.8 5.8	5.8		5.8 6.0	5.5	
				Bottom	10	26.8 26.8	26.8	7.7 8.2	8.0	32.1 31.9	32.0	90.6 90.8	90.7	6.7 6.7	6.7		5.8 5.8	5.8		13.0 13.0	13.0	
15-Oct-08	Sunny	Calm	13:01	Surface	1	27.2 27.4	27.3	8.0 7.3	7.7	28.1 28.1	28.1	88.8 91.4	90.1	6.6 6.8	6.7	7.0	3.0 2.9	3.0	3.7	9.0 9.0	9.0	13.8
				Middle	5.5	26.6 26.6	26.6	8.8 8.7	8.8	28.6 29.0	28.8	102.1 98.2	100.2	7.2 7.1	7.2		3.5 3.7	3.6		12.0 11.0	11.5	
				Bottom	10	26.0 25.9	26.0	7.3 8.5	7.9	29.2 29.2	29.2	80.6 80.8	80.7	6.5 6.5	6.5		4.6 4.3	4.5		21.0 21.0	21.0	
17-Oct-08	Sunny	Calm	14:34	Surface	1	27.4 27.4	27.4	7.6 7.3	7.5	31.1 31.1	31.1	85.8 84.1	85.0	6.9 6.8	6.9	6.7	3.8 3.9	3.9	4.6	11.0 11.0	11.0	12.5
				Middle	5.5	27.0 27.0	27.0	8.1 7.9	8.0	31.1 31.2	31.2	78.5 76.8	77.7	6.4 6.3	6.4		4.6 4.8	4.7		14.0 14.0	14.0	
				Bottom	10	26.9 26.9	26.9	7.4 7.8	7.6	31.4 31.3	31.4	74.1 73.9	74.0	6.1 6.1	6.1		5.3 5.2	5.3		13.0 12.0	12.5	
20-Oct-08	Sunny	Calm	16:43	Surface	1	27.7 27.7	27.7	7.6 7.6	7.6	30.7 30.6	30.7	99.6 98.0	98.8	6.3 6.3	6.3	6.4	3.5 3.6	3.6	4.3	10.0 10.0	10.0	12.0
				Middle	5.5	27.1 27.0	27.1	8.0 7.9	8.0	30.9 30.9	30.9	89.8 87.3	88.6	6.4 6.4	6.4		4.3 4.4	4.4		14.0 14.0	14.0	
				Bottom	10	26.9 26.9	26.9	7.5 7.6	7.6	31.1 31.0	31.1	83.4 82.9	83.2	6.7 6.7	6.7		4.9 5.0	5.0		12.0 12.0	12.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

### Water Quality Monitoring Results at CE - Mid-Ebb Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
22-Oct-08	Sunny	Calm	08:45	Surface	1	27.2 27.3	27.3	7.6 7.7	7.7	31.3 31.3	31.3	93.9 94.1	94.0	6.4 6.4	6.4	6.3	3.9 4.0	4.0	4.5	11.0 11.0	11.0	10.8		
				Middle	5.5	26.9 26.9	26.9	7.7 7.7	7.7	31.3 31.3	31.3	88.8 89.9	89.4	6.2 6.2	6.2		4.6 4.7	4.7		4.6 4.9	4.9		12.0 12.0	12.0
				Bottom	10	26.8 26.8	26.8	7.5 7.7	7.6	31.6 31.4	31.5	84.5 84.3	84.4	6.2 6.2	6.2		4.9 4.9	4.9		9.0 10.0	9.5			
24-Oct-08	Sunny	Calm	09:00	Surface	1	27.2 27.5	27.5	7.7 7.1	7.4	31.0 31.0	31.0	86.7 85.0	85.9	6.5 6.5	6.5	6.6	3.1 3.2	3.2	3.8	7.0 7.0	7.0	11.8		
				Middle	5.5	27.0 27.0	27.0	8.3 8.3	8.3	31.1 31.1	31.1	78.8 76.9	77.9	6.5 6.6	6.6		3.9 3.8	3.9		12.0 12.0	12.0			
				Bottom	10	26.9 26.8	26.9	7.2 7.9	7.6	31.3 31.2	31.3	73.9 73.6	73.8	6.8 6.8	6.8		4.2 4.3	4.3		17.0 16.0	16.5			
27-Oct-08	Sunny	Calm	12:03	Surface	1	26.6 26.6	26.6	8.1 7.7	7.9	30.8 30.8	30.8	98.1 96.5	97.3	6.3 6.2	6.3	6.3	3.3 3.4	3.4	4.0	9.0 9.0	9.0	9.7		
				Middle	5.5	26.0 26.0	26.0	8.7 8.7	8.7	31.0 31.0	31.0	89.3 87.1	88.2	6.3 6.3	6.3		4.1 4.1	4.1		12.0 12.0	12.0			
				Bottom	10	25.9 25.9	25.9	7.7 8.3	8.0	31.2 31.1	31.2	83.6 83.2	83.4	6.6 6.6	6.6		4.5 4.6	4.6		8.0 8.0	8.0			
29-Oct-08	Sunny	Calm	13:16	Surface	1	27.0 27.0	27.0	7.8 8.0	7.9	30.9 30.9	30.9	92.4 92.7	92.6	6.3 6.4	6.4	6.4	3.2 3.3	3.3	3.6	11.0 11.0	11.0	12.0		
				Middle	5.5	26.5 26.5	26.5	7.8 7.8	7.8	31.0 31.0	31.0	84.0 82.0	83.0	6.3 6.3	6.3		3.6 3.7	3.7		12.0 12.0	12.0			
				Bottom	10	26.4 26.3	26.4	7.9 8.1	8.0	31.3 31.1	31.2	78.7 78.4	78.6	6.5 6.6	6.6		3.8 3.8	3.8		13.0 13.0	13.0			
31-Oct-08	Sunny	Calm	09:02	Surface	1	26.9 26.9	26.9	8.2 7.7	8.0	31.4 31.4	31.4	96.8 97.0	96.9	6.5 6.5	6.5	6.4	4.7 4.8	4.8	5.1	8.0 8.0	8.0	12.0		
				Middle	5.5	26.6 26.6	26.6	8.3 8.3	8.3	31.7 31.7	31.7	88.9 88.7	88.8	6.2 6.1	6.2		5.0 5.1	5.1		12.0 12.0	12.0			
				Bottom	10	26.6 26.6	26.6	7.8 8.0	7.9	31.7 31.8	31.8	84.6 84.6	84.6	6.1 6.1	6.1		5.4 5.4	5.4		16.0 16.0	16.0			

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

### Water Quality Monitoring Results at CF - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
2-Oct-08	Sunny	Calm	08:10	Surface	1	27.7 27.6	27.7	7.9 8.4	8.2	27.3 27.4	27.4	125.8 125.7	125.8	8.9 8.9	8.9	8.9	2.3 2.2	2.3	2.8	8.0 8.0	8.0	11.5			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
				Bottom	3	27.5 27.4	27.5	8.7 8.4	8.6	27.3 27.4	27.4	122.4 121.2	121.8	8.5 8.7	8.6		8.6	3.2 3.2		3.2	3.2		15.0 15.0	15.0	
4-Oct-08	Cloudy	Calm	09:35	Surface	1	27.5 27.8	27.7	7.9 8.3	8.1	27.3 27.4	27.4	115.6 115.6	115.6	8.0 7.9	8.0	8.0	2.2 2.2	2.2	2.7	9.0 10.0	9.5	10.3			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	27.7 27.4	27.6	8.7 8.4	8.6	27.3 27.4	27.4	122.4 121.2	121.8	8.7 8.6	8.7		8.7	3.2 3.1		3.2	3.2		11.0 11.0	11.0	
6-Oct-08	Cloudy	Calm	08:15	Surface	1	26.0 26.0	26.0	7.4 7.7	7.6	29.6 29.2	29.4	84.4 84.3	84.4	6.5 6.4	6.5	6.5	1.8 1.9	1.9	2.2	7.0 6.0	6.5	0.0			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	25.5 25.5	25.5	8.2 7.8	8.0	30.2 30.2	30.2	77.6 77.0	77.3	6.1 6.0	6.1		6.1	2.4 2.4		2.4	2.4		13.0 13.0	13.0	
10-Oct-08	Sunny	Calm	16:37	Surface	1	27.0 26.9	27.0	8.1 8.5	8.3	29.4 29.3	29.4	92.8 103.4	98.1	6.8 7.5	7.2	7.2	1.5 1.5	1.5	2.2	10.0 10.0	10.0	13.0			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	26.3 26.3	26.3	8.3 8.3	8.3	30.4 30.4	30.4	81.7 81.8	81.8	6.1 6.1	6.1		6.1	2.8 2.8		2.8	2.8		16.0 16.0	16.0	
13-Oct-08	Sunny	Calm	18:11	Surface	1	26.7 26.8	26.8	7.6 8.0	7.8	31.1 31.2	31.2	105.3 104.0	104.7	7.8 7.7	7.8	7.8	3.0 2.8	2.9	3.1	10.0 9.0	9.5	10.8			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	26.8 26.8	26.8	8.3 8.1	8.2	31.6 31.6	31.6	102.3 102.2	102.3	7.5 7.5	7.5		7.5	3.2 3.1		3.2	3.2		12.0 12.0	12.0	
15-Oct-08	Fine	Calm	18:03	Surface	1	27.5 27.8	27.7	7.7 8.4	8.1	27.2 27.4	27.3	105.8 105.7	105.8	7.0 6.8	6.9	6.9	2.4 2.2	2.3	3.1	11.0 10.0	10.5	11.8			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	27.7 27.4	27.6	8.8 8.2	8.5	27.3 27.3	27.3	102.3 101.4	101.9	6.5 6.6	6.6		6.6	3.8 3.8		3.8	3.8		13.0 13.0	13.0	
17-Oct-08	Sunny	Calm	08:15	Surface	1	27.3 27.4	27.4	7.6 8.0	7.8	30.7 30.8	30.8	88.2 87.4	87.8	7.1 7.0	7.1	7.1	2.9 2.7	2.8	3.1	11.0 11.0	11.0	11.5			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	27.3 27.3	27.3	8.1 8.0	8.1	31.0 31.0	31.0	86.2 86.1	86.2	6.9 6.9	6.9		6.9	3.3 3.4		3.4	3.4		12.0 12.0	12.0	
20-Oct-08	Sunny	Calm	11:38	Surface	1	27.6 27.6	27.6	7.8 8.0	7.9	30.6 30.6	30.6	97.2 96.6	96.9	6.6 6.6	6.6	6.6	2.9 2.9	2.9	3.2	9.0 10.0	9.5	10.3			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	27.6 27.2	27.6	7.8 8.0	7.9	30.7 30.7	30.7	95.7 95.5	95.6	6.4 6.3	6.4		6.4	3.4 3.5		3.5	3.5		11.0 11.0	11.0	
24-Oct-08	Sunny	Calm	16:50	Surface	1	27.2 27.2	27.2	7.5 7.9	7.7	30.8 30.9	30.9	88.7 87.8	88.3	7.0 6.9	7.0	7.0	2.9 3.0	3.0	3.3	14.0 14.0	14.0	13.5			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	27.2 27.2	27.2	8.1 7.9	8.0	31.2 31.2	31.2	86.5 86.3	86.4	6.8 6.7	6.8		6.8	3.5 3.6		3.6	3.6		13.0 13.0	13.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at CF - Mid-Flood Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
27-Oct-08	Fine	Calm	17:11	Surface	1	26.4 26.4	26.4	8.0 8.4	8.2	30.7 30.8	30.8	97.9 97.2	97.6	6.6 6.6	6.6	6.6	2.5 2.5	2.5	2.9	14.0 14.0	14.0	13.8			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
				Bottom	3	26.4 26.4	26.4	8.5 8.4	8.5	30.9 30.9	30.9	96.1 95.9	96.0	6.4 6.4	6.4		6.4	6.4		3.2 3.2	3.2		14.0 13.0	13.5	
29-Oct-08	Fine	Calm	17:40	Surface	1	26.8 26.8	26.8	7.6 7.8	7.7	30.7 30.8	30.8	93.3 92.5	92.9	6.6 6.6	6.6	6.6	2.3 2.4	2.4	3.0	11.0 11.0	11.0	12.0			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	26.8 26.8	26.8	7.9 7.8	7.9	31.0 31.0	31.0	91.3 91.1	91.2	6.4 6.4	6.4		6.4	6.4		3.5 3.6	3.6		13.0 13.0	13.0	
31-Oct-08	Sunny	Calm	13:35	Surface	1	26.7 26.8	26.8	8.0 8.4	8.2	30.9 31.0	31.0	99.3 98.2	98.8	6.7 6.6	6.7	6.7	3.7 3.6	3.7	3.6	14.0 14.0	14.0	11.8			
				Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
				Bottom	3	26.7 26.7	26.7	8.3 8.4	8.4	31.3 31.3	31.3	96.8 96.6	96.7	6.5 6.5	6.5		6.5	6.5		3.4 3.5	3.5		10.0 9.0	9.5	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

### Water Quality Monitoring Results at I1 - Mid-Ebb Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	14:17	Surface	1	27.5 27.6	27.6	7.9 8.3	8.1	27.5 27.3	27.4	113.2 118.5	115.9	7.9 8.4	8.2	7.6	2.1 2.2	2.2	2.6	8.0 8.0	8.0	9.7
				Middle	4.5	26.6 26.9	26.8	7.6 8.0	7.8	27.9 27.9	27.9	97.4 94.6	96.0	7.1 6.9	7.0		2.4 2.4	2.4		13.0 13.0	13.0	
				Bottom	8	26.3 26.1	26.2	8.2 8.4	8.3	28.5 29.3	28.9	86.9 86.1	86.5	6.5 6.4	6.5		2.8 3.4	3.1		8.0 8.0	8.0	
4-Oct-08	Cloudy	Calm	15:11	Surface	1	27.5 27.5	27.5	7.9 8.5	8.2	27.3 27.4	27.4	113.1 118.6	115.9	7.9 8.2	8.1	7.6	2.1 2.2	2.2	2.6	8.0 8.0	8.0	9.0
				Middle	4.5	26.6 26.8	26.7	7.8 8.0	7.9	27.8 27.9	27.9	97.5 94.6	96.1	7.0 6.9	7.0		2.4 2.3	2.4		10.0 10.0	10.0	
				Bottom	8	26.5 26.2	26.4	8.2 8.2	8.2	28.5 29.2	28.9	86.9 79.9	83.4	6.4 6.1	6.3		2.9 3.4	3.2		9.0 9.0	9.0	
6-Oct-08	Cloudy	Calm	17:30	Surface	1	25.7 25.7	25.7	7.3 7.8	7.6	28.9 28.9	28.9	93.3 92.2	92.8	7.1 7.0	7.1	6.8	2.2 2.3	2.3	2.5	10.0 10.0	10.0	11.3
				Middle	4.5	25.3 25.3	25.3	7.2 7.4	7.3	29.7 29.8	29.8	85.3 84.4	84.9	6.5 6.5	6.5		2.5 2.5	2.5		14.0 14.0	14.0	
				Bottom	8	25.1 25.1	25.1	7.8 7.8	7.8	30.2 30.2	30.2	79.2 79.2	79.2	6.1 6.1	6.1		2.7 2.8	2.8		10.0 10.0	10.0	
8-Oct-08	Sunny	Calm	08:46	Surface	1	25.4 25.5	25.5	8.3 8.0	8.2	31.8 31.9	31.9	87.4 88.0	87.7	6.3 6.4	6.4	6.5	2.6 2.5	2.6	2.6	10.0 10.0	10.0	10.3
				Middle	4.5	25.3 25.4	25.4	7.9 8.5	8.2	31.8 31.8	31.8	89.7 90.0	89.9	6.6 6.6	6.6		2.4 2.6	2.5		12.0 12.0	12.0	
				Bottom	8	25.0 25.0	25.0	8.1 8.3	8.2	32.1 31.9	32.0	89.9 89.9	89.9	6.6 6.6	6.6		2.8 2.8	2.8		9.0 9.0	9.0	
10-Oct-08	Sunny	Calm	09:42	Surface	1	26.6 26.6	26.6	8.0 8.4	8.2	28.2 28.2	28.2	109.2 110.7	110.0	8.1 8.2	8.2	7.6	1.9 1.8	1.9	2.5	12.0 12.0	12.0	13.5
				Middle	4.5	26.3 26.3	26.3	7.7 7.9	7.8	28.8 28.8	28.8	94.1 91.8	93.0	7.1 6.9	7.0		2.3 2.4	2.4		15.0 17.0	16.0	
				Bottom	8	25.5 25.5	25.5	8.3 8.1	8.2	29.3 29.3	29.3	85.6 85.1	85.4	6.5 6.5	6.5		3.1 3.2	3.2		12.0 13.0	12.5	
13-Oct-08	Sunny	Calm	11:31	Surface	1	26.8 26.8	26.8	7.9 7.8	7.9	32.0 32.0	32.0	93.4 92.5	93.0	6.9 6.9	6.9	6.9	3.2 3.2	3.2	3.5	10.0 10.0	10.0	12.3
				Middle	4.5	26.8 26.8	26.8	8.2 7.6	7.9	32.1 32.0	32.1	91.2 91.2	91.2	6.8 6.8	6.8		3.6 3.5	3.6		12.0 12.0	12.0	
				Bottom	8	26.8 26.8	26.8	8.0 7.8	7.9	31.6 32.2	31.9	91.8 92.1	92.0	6.8 6.8	6.8		3.6 3.5	3.6		15.0 15.0	15.0	
15-Oct-08	Sunny	Calm	12:47	Surface	1	27.6 27.5	27.6	7.6 8.3	8.0	27.3 27.4	27.4	95.3 95.3	95.3	6.8 6.8	6.8	6.8	2.2 2.1	2.2	2.6	18.0 18.0	18.0	12.2
				Middle	4.5	26.7 27.0	26.9	7.7 8.0	7.9	27.9 27.8	27.9	94.5 94.5	94.5	6.8 6.8	6.8		2.4 2.5	2.5		9.0 9.0	9.0	
				Bottom	8	26.4 26.2	26.3	8.2 8.2	8.2	28.5 29.2	28.9	86.8 80.0	83.4	6.4 6.0	6.2		2.8 3.2	3.0		9.0 10.0	9.5	
17-Oct-08	Sunny	Calm	14:16	Surface	1	27.3 27.3	27.3	7.8 7.8	7.8	31.1 31.1	31.1	85.0 82.3	83.7	6.8 6.7	6.8	6.7	2.9 2.9	2.9	3.2	10.0 10.0	10.0	11.7
				Middle	4.5	27.2 27.2	27.2	7.7 7.4	7.6	31.2 31.1	31.2	79.9 79.5	79.7	6.5 6.5	6.5		3.2 3.1	3.2		12.0 12.0	12.0	
				Bottom	8	27.0 27.0	27.0	8.0 7.8	7.9	31.0 31.3	31.2	77.4 76.8	77.1	6.4 6.3	6.4		3.4 3.6	3.5		13.0 13.0	13.0	
20-Oct-08	Sunny	Calm	16:20	Surface	1	27.6 27.6	27.6	8.1 7.7	7.9	30.6 30.6	30.6	98.3 94.7	96.5	6.3 6.4	6.4	6.5	2.7 2.8	2.8	3.1	6.0 6.0	6.0	11.7
				Middle	4.5	27.4 27.4	27.4	7.9 7.8	7.9	30.7 30.7	30.7	91.7 91.1	91.4	6.6 6.6	6.6		3.1 3.0	3.1		15.0 15.0	15.0	
				Bottom	8	27.2 27.1	27.2	7.7 7.7	7.7	30.7 30.9	30.8	87.7 86.7	87.2	6.5 6.4	6.5		3.3 3.5	3.4		14.0 14.0	14.0	

Remarks: \* DA: Depth-Averaged

\*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at I1 - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
22-Oct-08	Sunny	Calm	08:23	Surface	1	27.2 27.2	27.2	7.7 7.5	7.6	31.3 31.3	31.3	98.9 99.7	99.3	6.6 6.7	6.7	6.5	3.0 3.0	3.0	3.3	5.0 5.0	5.0	6.0
				Middle	4.5	27.1 27.1	27.1	7.6 7.7	7.7	31.4 31.3	31.4	88.9 88.6	88.8	6.2 6.2	6.2		3.4 3.3	3.4		6.0 6.0	6.0	
				Bottom	8	27.0 27.0	27.0	7.5 7.5	7.5	31.2 31.5	31.4	87.2 86.9	87.1	6.2 6.1	6.2		3.5 3.5	3.5		7.0 7.0	7.0	
24-Oct-08	Sunny	Calm	09:24	Surface	1	27.4 27.4	27.4	7.4 7.9	7.7	31.0 31.0	31.0	85.8 82.9	84.4	6.4 6.6	6.5	6.6	2.8 2.7	2.8	3.1	6.0 7.0	6.5	9.5
				Middle	4.5	27.3 27.2	27.3	7.2 7.5	7.4	31.1 31.0	31.1	80.3 79.8	80.1	6.7 6.7	6.7		3.2 3.2	3.2		9.0 9.0	9.0	
				Bottom	8	27.1 27.0	27.1	7.8 7.7	7.8	30.9 31.2	31.1	77.4 76.8	77.1	6.6 6.5	6.6		3.3 3.3	3.3		13.0 13.0	13.0	
27-Oct-08	Sunny	Calm	11:39	Surface	1	26.5 26.5	26.5	7.9 8.4	8.2	30.8 30.8	30.8	97.0 93.8	95.4	6.2 6.3	6.3	6.4	2.7 2.7	2.7	3.1	10.0 10.0	10.0	10.0
				Middle	4.5	26.3 26.3	26.3	7.7 8.0	7.9	30.9 30.9	30.9	91.0 90.4	90.7	6.5 6.5	6.5		3.1 3.1	3.1		9.0 9.0	9.0	
				Bottom	8	26.1 26.1	26.1	8.3 8.2	8.3	30.8 31.0	30.9	87.5 86.7	87.1	6.4 6.3	6.4		3.3 3.4	3.4		11.0 11.0	11.0	
29-Oct-08	Sunny	Calm	12:51	Surface	1	26.9 26.9	26.9	8.1 7.7	7.9	30.9 30.9	30.9	91.4 88.3	89.9	6.2 6.3	6.3	6.4	2.7 2.7	2.7	3.0	12.0 12.0	12.0	14.3
				Middle	4.5	26.8 26.8	26.8	8.0 7.9	8.0	31.0 30.9	31.0	85.6 85.1	85.4	6.4 6.4	6.4		3.1 3.1	3.1		15.0 15.0	15.0	
				Bottom	8	26.6 26.6	26.6	7.9 8.1	8.0	30.9 31.1	31.0	82.5 81.7	82.1	6.4 6.3	6.4		3.3 3.3	3.3		16.0 16.0	16.0	
31-Oct-08	Sunny	Calm	08:46	Surface	1	26.8 26.9	26.9	8.2 8.1	8.2	31.4 31.5	31.5	98.4 98.8	98.6	6.6 6.7	6.7	6.4	3.9 3.8	3.9	4.3	13.0 12.0	12.5	9.5
				Middle	4.5	26.8 26.8	26.8	8.1 8.1	8.1	31.5 31.6	31.6	88.4 88.1	88.3	6.1 6.1	6.1		4.3 4.3	4.3		8.0 8.0	8.0	
				Bottom	8	26.7 26.7	26.7	8.1 8.0	8.1	31.8 31.9	31.9	87.1 86.9	87.0	6.1 6.0	6.1		4.5 4.6	4.6		8.0 8.0	8.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher



### Water Quality Monitoring Results at I1 - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	08:36	Surface	1	27.4 27.5	27.5	7.8 7.9	7.9	27.7 27.5	27.6	88.4 88.4	88.4	6.4 6.4	6.4	6.7	2.6 2.6	2.6	2.9	11.0 11.0	11.0	13.7
				Middle	4.5	26.5 26.4	26.5	8.5 7.7	8.1	28.5 28.7	28.6	105.0 86.7	95.9	7.4 6.5	7.0		2.7 2.8	2.8		12.0 12.0	12.0	
				Bottom	8	25.8 25.8	25.8	7.7 8.6	8.2	29.4 29.5	29.5	76.6 76.8	76.7	6.1 6.1	6.1		3.1 3.7	3.4		18.0 18.0	18.0	
4-Oct-08	Cloudy	Calm	10:01	Surface	1	27.4 27.3	27.4	7.7 7.9	7.8	27.6 27.4	27.5	88.7 88.3	88.5	6.5 6.5	6.5	7.0	2.6 2.4	2.5	2.9	10.0 10.0	10.0	11.7
				Middle	4.5	26.6 26.2	26.4	8.3 7.8	8.1	28.5 28.7	28.6	105.0 105.8	105.4	7.4 7.4	7.4		2.6 2.8	2.7		11.0 11.0	11.0	
				Bottom	8	26.0 26.0	26.0	7.8 8.7	8.3	29.3 29.5	29.4	72.2 72.4	72.3	6.1 6.1	6.1		3.2 3.5	3.4		14.0 14.0	14.0	
6-Oct-08	Cloudy	Calm	08:27	Surface	1	25.0 25.0	25.0	7.3 7.4	7.4	31.0 31.0	31.0	86.3 93.1	89.7	7.0 7.1	7.1	7.1	2.4 2.4	2.4	2.5	11.0 11.0	11.0	10.3
				Middle	4.5	25.9 25.9	25.9	8.0 7.2	7.6	29.6 29.6	29.6	94.5 90.6	92.6	7.1 6.9	7.0		2.5 2.3	2.4		13.0 13.0	13.0	
				Bottom	8	25.8 25.8	25.8	7.4 8.1	7.8	29.6 29.6	29.6	89.8 80.8	85.3	6.8 6.2	6.5		2.7 2.8	2.8		8.0 8.0	8.0	
10-Oct-08	Sunny	Calm	17:08	Surface	1	26.9 26.9	26.9	7.7 7.8	7.8	31.3 31.4	31.4	93.4 92.8	93.1	6.9 6.8	6.9	6.9	1.9 1.9	1.9	2.5	15.0 15.0	15.0	15.0
				Middle	4.5	26.8 26.9	26.9	8.2 7.8	8.0	31.5 31.6	31.6	93.1 92.0	92.6	6.8 6.8	6.8		2.4 2.5	2.5		15.0 15.0	15.0	
				Bottom	8	27.2 27.2	27.2	7.9 8.7	8.3	32.0 32.0	32.0	92.7 93.6	93.2	6.9 6.9	6.9		2.9 3.1	3.0		15.0 15.0	15.0	
13-Oct-08	Sunny	Calm	17:53	Surface	1	26.6 26.4	26.5	7.4 7.6	7.5	29.5 32.3	30.9	102.9 108.0	105.5	7.7 7.9	7.8	7.5	2.9 2.9	2.9	3.2	9.0 9.0	9.0	12.7
				Middle	4.5	26.8 26.8	26.8	7.9 7.9	7.9	32.3 32.0	32.2	96.7 96.7	96.7	7.1 7.1	7.1		3.2 3.3	3.3		15.0 15.0	15.0	
				Bottom	8	26.8 26.8	26.8	7.9 8.0	8.0	32.1 32.2	32.2	96.8 96.8	96.8	7.1 7.1	7.1		3.4 3.4	3.4		14.0 14.0	14.0	
15-Oct-08	Fine	Calm	18:28	Surface	1	27.4 27.5	27.5	7.7 8.0	7.9	27.7 27.4	27.6	88.4 88.4	88.4	6.5 6.5	6.5	6.8	2.6 2.5	2.6	2.9	9.0 9.0	9.0	9.5
				Middle	4.5	26.7 26.2	26.5	8.3 7.7	8.0	28.4 28.7	28.6	104.9 86.7	95.8	7.6 6.6	7.1		2.7 2.7	2.7		13.0 13.0	13.0	
				Bottom	8	25.8 25.8	25.8	7.9 8.5	8.2	29.4 29.4	29.4	78.7 72.2	75.5	6.2 6.0	6.1		3.1 3.5	3.3		7.0 6.0	6.5	
17-Oct-08	Sunny	Calm	08:48	Surface	1	27.2 27.1	27.2	7.6 7.5	7.6	29.9 31.2	30.6	83.2 86.0	84.6	6.8 6.9	6.9	6.7	2.8 2.7	2.8	3.2	10.0 10.0	10.0	10.3
				Middle	4.5	27.0 27.0	27.0	7.7 7.8	7.8	31.3 31.2	31.3	80.1 79.8	80.0	6.5 6.5	6.5		3.1 3.3	3.2		11.0 11.0	11.0	
				Bottom	8	26.8 26.8	26.8	7.8 8.1	8.0	31.2 31.3	31.3	79.2 79.2	79.2	6.5 6.5	6.5		3.4 3.6	3.5		10.0 10.0	10.0	
20-Oct-08	Sunny	Calm	12:19	Surface	1	27.5 27.5	27.5	8.1 7.5	7.8	30.1 30.7	30.4	90.9 92.5	91.7	7.0 6.2	6.6	6.5	2.9 2.8	2.9	3.2	12.0 12.0	12.0	12.2
				Middle	4.5	27.3 27.3	27.3	7.1 8.1	7.6	30.8 30.8	30.8	89.3 88.9	89.1	6.3 6.4	6.4		3.1 3.3	3.2		12.0 12.0	12.0	
				Bottom	8	27.1 27.1	27.1	8.2 7.8	8.0	30.8 30.8	30.8	87.9 87.9	87.9	6.6 6.6	6.6		3.4 3.8	3.6		13.0 12.0	12.5	
24-Oct-08	Sunny	Calm	16:16	Surface	1	27.0 26.9	27.0	7.3 7.4	7.4	29.8 31.5	30.7	84.4 87.7	86.1	7.1 6.9	7.0	6.8	2.6 2.7	2.7	3.1	13.0 13.0	13.0	12.7
				Middle	4.5	27.1 27.0	27.1	7.9 7.3	7.6	31.5 31.4	31.5	80.5 80.3	80.4	6.5 6.6	6.6		3.0 3.1	3.1		14.0 14.0	14.0	
				Bottom	8	27.0 26.9	27.0	7.4 8.2	7.8	31.4 31.5	31.5	79.8 79.8	79.8	5.6 6.7	6.2		3.3 3.4	3.4		11.0 11.0	11.0	

Remarks: \* DA: Depth-Averaged

\*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at I1 - Mid-Flood Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
27-Oct-08	Fine	Calm	17:46	Surface	1	26.2 26.2	26.2	7.7 7.9	7.8	29.9 31.1	30.5	92.6 95.1	93.9	6.9 6.4	6.7	6.5	2.7 2.7	2.7	3.1	10.0 10.0	10.0	10.3
				Middle	4.5	26.2 26.2	26.2	8.3 7.8	8.1	31.2 31.1	31.2	89.9 89.6	89.8	6.2 6.3	6.3		3.0 3.2	3.1		9.0 9.0	9.0	
				Bottom	8	26.0 26.0	26.0	7.9 8.7	8.3	31.1 31.2	31.2	88.8 88.8	88.8	6.5 6.5	6.5		3.3 3.6	3.5		12.0 12.0	12.0	
29-Oct-08	Fine	Calm	18:14	Surface	1	26.6 26.6	26.6	7.5 7.6	7.6	29.9 31.3	30.6	88.5 91.4	90.0	6.8 6.5	6.7	6.5	2.5 2.7	2.6	3.0	13.0 13.0	13.0	12.2
				Middle	4.5	26.6 26.6	26.6	7.7 7.7	7.7	31.3 31.2	31.3	85.2 84.9	85.1	6.2 6.3	6.3		3.0 3.1	3.1		14.0 14.0	14.0	
				Bottom	8	26.5 26.4	26.5	7.7 7.8	7.8	31.3 31.3	31.3	84.3 84.3	84.3	6.1 6.4	6.3		3.3 3.5	3.4		9.0 10.0	9.5	
31-Oct-08	Sunny	Calm	14:17	Surface	1	26.9 26.9	26.9	8.2 8.0	8.1	31.2 31.3	31.3	95.7 99.7	97.7	6.8 6.7	6.8	6.5	3.7 3.8	3.8	4.1	7.0 7.0	7.0	11.3
				Middle	4.5	26.7 26.7	26.7	7.7 8.1	7.9	31.7 31.7	31.7	90.9 90.8	90.9	6.2 6.2	6.2		4.1 4.2	4.2		12.0 12.0	12.0	
				Bottom	8	26.6 26.6	26.6	8.2 8.2	8.2	31.8 31.8	31.8	95.5 90.5	93.0	6.6 6.3	6.5		4.4 4.4	4.4		15.0 15.0	15.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at I2 - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	14:10	Surface	1	27.7 27.6	27.7	8.3 8.1	8.2	27.4 27.5	27.5	109.8 121.6	115.7	7.7 8.7	8.2	8.2	2.2 2.1	2.2	2.4	6.0 6.0	6.0	10.0
				Middle	4.5	27.1 26.8	27.0	8.4 8.0	8.2	27.6 27.7	27.7	124.1 102.5	113.3	8.7 7.4	8.1		2.1 2.2	2.2		12.0 12.0	12.0	
				Bottom	8	26.2 26.3	26.3	8.7 8.1	8.4	28.7 28.6	28.7	90.5 90.5	90.5	6.6 6.6	6.6		2.7 2.8	2.8		12.0 12.0	12.0	
4-Oct-08	Cloudy	Calm	15:05	Surface	1	27.7 27.5	27.6	8.4 8.0	8.2	27.2 27.4	27.3	109.6 107.7	108.7	7.8 7.7	7.8	7.7	2.2 2.1	2.2	2.4	7.0 8.0	7.5	7.3
				Middle	4.5	27.2 27.0	27.1	8.6 7.9	8.3	27.7 27.5	27.6	102.4 102.0	102.2	7.6 7.6	7.6		2.0 2.3	2.2		6.0 7.0	6.5	
				Bottom	8	26.4 26.4	26.4	8.6 8.1	8.4	28.7 28.5	28.6	90.6 82.2	86.4	6.6 6.1	6.4		2.7 2.7	2.7		8.0 8.0	8.0	
6-Oct-08	Cloudy	Calm	17:41	Surface	1	25.8 25.8	25.8	7.9 7.5	7.7	29.2 29.2	29.2	98.6 96.9	97.8	7.4 7.3	7.4	7.0	2.3 2.2	2.3	2.5	8.0 8.0	8.0	10.0
				Middle	4.5	25.6 25.6	25.6	8.1 7.4	7.8	29.9 29.9	29.9	88.3 84.7	86.5	6.7 6.5	6.6		2.6 2.4	2.5		10.0 10.0	10.0	
				Bottom	8	25.3 25.3	25.3	8.1 7.4	7.8	30.4 30.4	30.4	79.0 77.8	78.4	6.1 6.0	6.1		2.7 2.7	2.7		12.0 12.0	12.0	
8-Oct-08	Sunny	Calm	08:36	Surface	1	25.5 25.5	25.5	8.1 8.0	8.1	31.3 31.4	31.4	89.3 88.4	88.9	6.4 6.5	6.5	6.5	2.5 2.4	2.5	2.7	8.0 9.0	8.5	11.8
				Middle	4.5	25.5 25.5	25.5	8.4 7.9	8.2	31.3 31.4	31.4	88.4 87.8	88.1	6.4 6.3	6.4		2.6 2.6	2.6		15.0 15.0	15.0	
				Bottom	8	25.3 25.2	25.3	8.5 8.1	8.3	31.5 31.6	31.6	88.1 87.0	87.6	6.3 6.3	6.3		2.9 3.1	3.0		12.0 12.0	12.0	
10-Oct-08	Sunny	Calm	09:36	Surface	1	27.1 27.1	27.1	8.5 7.9	8.2	28.1 28.1	28.1	94.3 95.6	95.0	7.1 7.1	7.1	7.1	1.2 1.3	1.3	1.7	12.0 12.0	12.0	14.2
				Middle	4.5	26.5 26.4	26.5	8.5 7.9	8.2	28.4 28.4	28.4	97.2 96.9	97.1	7.1 7.1	7.1		1.6 1.6	1.6		14.0 15.0	14.5	
				Bottom	8	26.2 26.2	26.2	8.3 8.0	8.2	29.9 29.9	29.9	77.3 76.5	76.9	6.1 6.0	6.1		2.1 2.2	2.2		16.0 16.0	16.0	
13-Oct-08	Sunny	Calm	11:21	Surface	1	26.6 26.7	26.7	7.7 8.0	7.9	32.3 32.2	32.3	108.8 105.2	107.0	8.0 7.7	7.9	7.6	2.6 2.8	2.7	3.0	13.0 13.0	13.0	12.0
				Middle	4.5	26.8 26.8	26.8	7.5 7.6	7.6	32.2 32.2	32.2	98.3 98.3	98.3	7.2 7.2	7.2		3.1 3.1	3.1		12.0 12.0	12.0	
				Bottom	8	26.8 26.8	26.8	8.0 7.9	8.0	32.3 32.3	32.3	98.8 98.8	98.8	7.3 7.3	7.3		3.3 3.3	3.3		11.0 11.0	11.0	
15-Oct-08	Sunny	Calm	12:41	Surface	1	27.8 27.6	27.7	8.4 8.0	8.2	27.2 27.4	27.3	109.6 111.7	110.7	7.7 7.8	7.8	7.3	2.3 2.0	2.2	2.3	13.0 13.0	13.0	15.2
				Middle	4.5	27.1 26.8	27.0	8.5 8.0	8.3	27.5 27.7	27.6	94.0 94.5	94.3	6.7 6.8	6.8		2.0 2.2	2.1		15.0 14.0	14.5	
				Bottom	8	26.4 26.4	26.4	8.7 7.8	8.3	28.5 28.5	28.5	84.6 82.3	83.5	6.3 6.2	6.3		2.6 2.8	2.7		18.0 18.0	18.0	
17-Oct-08	Sunny	Calm	14:06	Surface	1	27.3 27.3	27.3	7.7 7.9	7.8	31.2 31.2	31.2	91.4 88.3	89.9	7.3 7.0	7.2	6.9	2.7 2.5	2.6	2.9	13.0 14.0	13.5	14.2
				Middle	4.5	27.1 27.1	27.1	7.8 7.4	7.6	31.3 31.3	31.3	80.9 80.9	80.9	6.6 6.6	6.6		2.8 2.9	2.9		14.0 14.0	14.0	
				Bottom	8	27.0 27.0	27.0	7.9 7.8	7.9	31.4 31.4	31.4	79.6 79.4	79.5	6.5 6.5	6.5		3.1 3.2	3.2		15.0 15.0	15.0	
20-Oct-08	Sunny	Calm	16:15	Surface	1	27.6 27.6	27.6	7.8 7.7	7.8	30.7 30.7	30.7	100.2 97.4	98.8	6.4 6.5	6.5	6.5	2.8 2.8	2.8	2.9	10.0 10.0	10.0	12.8
				Middle	4.5	27.3 27.3	27.3	8.0 7.5	7.8	30.8 30.8	30.8	89.7 89.7	89.7	6.6 6.3	6.5		2.7 2.8	2.8		13.0 13.0	13.0	
				Bottom	8	27.1 27.1	27.1	7.7 7.9	7.8	31.0 31.0	31.0	87.5 87.2	87.4	6.4 6.3	6.4		3.1 3.2	3.2		16.0 15.0	15.5	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at I2 - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
22-Oct-08	Sunny	Calm	08:16	Surface	1	27.1 27.1	27.1	7.5 7.5	7.5	31.5 31.5	31.5	102.0 98.8	100.4	6.7 6.6	6.7	6.6	2.7 2.8	2.8	3.0	8.0 8.0	8.0	12.0
				Middle	4.5	27.0 27.0	27.0	7.9 7.7	7.8	31.5 31.5	31.5	91.5 91.5	91.5	6.4 6.3	6.4		2.9 3.0	3.0		17.0 17.0	17.0	
				Bottom	8	26.9 26.9	26.9	7.7 7.5	7.6	31.6 31.7	31.7	90.6 90.5	90.6	6.3 6.3	6.3		3.2 3.3	3.3		11.0 11.0	11.0	
24-Oct-08	Sunny	Calm	09:33	Surface	1	27.3 27.3	27.3	8.0 7.5	7.8	31.1 31.1	31.1	91.1 88.1	89.6	6.8 6.9	6.9	6.8	2.5 2.5	2.5	2.9	12.0 12.0	12.0	13.7
				Middle	4.5	27.2 27.2	27.2	8.1 7.5	7.8	31.2 31.2	31.2	80.6 80.6	80.6	6.8 6.6	6.7		2.8 2.9	2.9		16.0 16.0	16.0	
				Bottom	8	27.0 27.0	27.0	8.1 7.5	7.8	31.3 31.3	31.3	79.0 78.8	78.9	6.7 6.6	6.7		3.1 3.2	3.2		13.0 13.0	13.0	
27-Oct-08	Sunny	Calm	11:31	Surface	1	26.5 26.5	26.5	8.4 8.0	8.2	30.9 30.9	30.9	100.6 97.7	99.2	6.5 6.5	6.5	6.5	2.6 2.6	2.6	2.9	10.0 10.0	10.0	11.3
				Middle	4.5	26.3 26.3	26.3	8.6 7.9	8.3	31.0 31.0	31.0	90.1 90.1	90.1	6.5 6.3	6.4		2.7 2.8	2.8		10.0 10.0	10.0	
				Bottom	8	26.1 26.1	26.1	8.5 8.0	8.3	31.2 31.2	31.2	88.2 88.0	88.1	6.4 6.3	6.4		3.1 3.2	3.2		14.0 14.0	14.0	
29-Oct-08	Sunny	Calm	12:43	Surface	1	26.9 26.9	26.9	7.9 7.9	7.9	31.0 31.0	31.0	95.8 92.9	94.4	6.5 6.5	6.5	6.5	2.5 2.5	2.5	2.8	13.0 13.0	13.0	14.0
				Middle	4.5	26.7 26.7	26.7	8.0 7.7	7.9	31.1 31.1	31.1	85.3 85.3	85.3	6.5 6.3	6.4		2.7 2.8	2.8		12.0 12.0	12.0	
				Bottom	8	26.5 26.5	26.5	8.2 8.0	8.1	31.2 31.3	31.3	83.6 83.4	83.5	6.4 6.3	6.4		3.1 3.2	3.2		17.0 17.0	17.0	
31-Oct-08	Sunny	Calm	08:30	Surface	1	26.7 26.8	26.8	8.3 7.9	8.1	31.6 31.6	31.6	102.3 99.0	100.7	6.7 6.6	6.7	6.6	3.5 3.6	3.6	3.9	14.0 14.0	14.0	14.3
				Middle	4.5	26.7 26.7	26.7	8.4 7.9	8.2	31.7 31.7	31.7	91.8 91.8	91.8	6.4 6.3	6.4		3.9 3.9	3.9		15.0 15.0	15.0	
				Bottom	8	26.7 26.7	26.7	8.1 8.1	8.1	31.8 31.8	31.8	91.2 91.1	91.2	6.3 6.3	6.3		4.2 4.3	4.3		14.0 14.0	14.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

### Water Quality Monitoring Results at I2 - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	08:30	Surface	1	27.6 27.7	27.7	7.8 7.9	7.9	27.3 27.2	27.3	105.7 105.7	105.7	7.4 7.4	7.4	7.1	2.3 2.1	2.2	2.5	10.0 10.0	10.0	12.7
				Middle	4.5	26.4 26.6	26.5	7.6 8.1	7.9	28.2 28.0	28.1	94.1 89.3	91.7	6.9 6.7	6.8		2.3 2.4	2.4		2.0 2.0	20.0	
				Bottom	8	26.3 26.1	26.2	7.7 7.7	7.7	29.1 29.0	29.1	76.0 76.5	76.3	6.1 6.2	6.2		2.8 3.1	3.0		8.0 8.0	8.0	
4-Oct-08	Cloudy	Calm	09:55	Surface	1	27.7 27.8	27.8	7.8 7.8	7.8	27.2 27.4	27.3	105.1 105.7	105.4	7.5 7.5	7.5	7.2	2.3 2.1	2.2	2.5	10.0 10.0	10.0	10.3
				Middle	4.5	26.6 26.8	26.7	7.6 7.9	7.8	28.1 27.9	28.0	94.0 89.2	91.6	7.0 6.5	6.8		2.3 2.5	2.4		9.0 9.0	9.0	
				Bottom	8	26.3 26.0	26.2	7.8 7.9	7.9	28.9 29.0	29.0	78.6 75.6	77.1	6.1 6.1	6.1		2.9 3.1	3.0		12.0 12.0	12.0	
6-Oct-08	Cloudy	Calm	08:39	Surface	1	25.6 25.5	25.6	7.4 7.3	7.4	30.1 30.2	30.2	84.8 84.6	84.7	7.8 7.8	7.8	7.4	2.3 2.4	2.4	2.6	11.0 11.0	11.0	11.8
				Middle	4.5	26.1 26.1	26.1	7.2 7.5	7.4	28.6 28.7	28.7	91.6 90.0	90.8	6.9 6.8	6.9		2.5 2.6	2.6		11.0 11.0	11.0	
				Bottom	8	25.6 25.6	25.6	7.2 7.2	7.2	30.0 30.0	30.0	80.6 78.1	79.4	6.2 6.0	6.1		2.7 2.6	2.7		9.0 10.0	9.5	
10-Oct-08	Sunny	Calm	16:58	Surface	1	26.9 26.9	26.9	7.7 7.7	7.7	29.5 31.5	30.5	93.4 93.4	93.4	6.9 6.9	6.9	6.9	1.7 1.8	1.8	2.0	14.0 14.0	14.0	15.3
				Middle	4.5	27.0 27.0	27.0	7.6 7.9	7.8	32.0 32.1	32.1	90.2 90.3	90.3	6.8 6.8	6.8		1.9 1.9	1.9		17.0 17.0	17.0	
				Bottom	8	27.2 27.2	27.2	7.6 7.7	7.7	31.3 31.4	31.4	94.3 93.4	93.9	6.9 7.0	7.0		2.3 2.4	2.4		15.0 15.0	15.0	
13-Oct-08	Sunny	Calm	17:41	Surface	1	26.7 26.8	26.8	7.4 7.5	7.5	32.2 32.1	32.2	109.1 105.0	107.1	8.0 7.7	7.9	7.6	3.4 3.3	3.4	3.2	9.0 9.0	9.0	11.2
				Middle	4.5	26.8 26.8	26.8	7.3 7.5	7.4	32.2 32.2	32.2	99.4 99.4	99.4	7.3 7.3	7.3		2.9 2.9	2.9		15.0 15.0	15.0	
				Bottom	8	26.8 26.8	26.8	7.4 7.5	7.5	32.2 32.2	32.2	99.5 99.5	99.5	7.3 7.3	7.3		3.2 3.3	3.3		9.0 10.0	9.5	
15-Oct-08	Fine	Calm	18:23	Surface	1	27.7 27.8	27.8	7.7 7.9	7.8	27.4 27.4	27.4	83.8 95.9	89.9	6.1 6.6	6.4	6.6	2.5 2.1	2.3	2.6	10.0 10.0	10.0	10.7
				Middle	4.5	26.4 26.7	26.6	7.6 7.9	7.8	28.1 28.1	28.1	94.2 89.2	91.7	7.0 6.6	6.8		2.5 2.4	2.5		11.0 11.0	11.0	
				Bottom	8	26.2 26.1	26.2	7.5 7.8	7.7	29.1 29.1	29.1	76.4 78.6	77.5	6.0 6.4	6.2		3.0 3.0	3.0		11.0 11.0	11.0	
17-Oct-08	Sunny	Calm	08:40	Surface	1	27.4 27.3	27.4	7.4 7.5	7.5	31.2 31.2	31.2	88.3 86.2	87.3	7.0 6.9	7.0	6.8	2.7 2.9	2.8	3.0	16.0 16.0	16.0	12.5
				Middle	4.5	27.1 27.1	27.1	7.2 7.4	7.3	31.3 31.3	31.3	82.0 80.3	81.2	6.6 6.5	6.6		2.9 2.8	2.9		11.0 11.0	11.0	
				Bottom	8	27.0 27.0	27.0	7.3 7.4	7.4	31.4 31.4	31.4	79.4 79.2	79.3	6.5 6.5	6.5		3.3 3.4	3.4		10.0 11.0	10.5	
20-Oct-08	Sunny	Calm	12:08	Surface	1	27.7 27.7	27.7	7.7 7.8	7.8	30.7 30.7	30.7	95.4 94.3	94.9	6.6 6.6	6.6	6.6	2.7 2.7	2.7	3.0	12.0 12.0	12.0	10.3
				Middle	4.5	27.3 27.3	27.3	7.5 7.4	7.5	30.8 30.8	30.8	90.8 88.3	89.6	6.6 6.6	6.6		2.9 2.8	2.9		11.0 11.0	11.0	
				Bottom	8	27.2 27.2	27.2	7.8 7.3	7.6	31.0 31.0	31.0	86.9 86.6	86.8	6.6 6.7	6.7		3.4 3.4	3.4		8.0 8.0	8.0	
24-Oct-08	Sunny	Calm	16:25	Surface	1	27.2 27.2	27.2	7.4 7.3	7.4	31.4 31.4	31.4	89.7 87.1	88.4	7.1 6.9	7.0	6.9	2.9 3.1	3.0	3.2	11.0 11.0	11.0	10.8
				Middle	4.5	27.0 27.0	27.0	7.1 7.5	7.3	31.5 31.5	31.5	82.6 81.3	82.0	6.8 6.7	6.8		3.3 3.3	3.3		9.0 10.0	9.5	
				Bottom	8	27.0 27.0	27.0	7.2 7.4	7.3	31.6 31.6	31.6	80.7 80.5	80.6	6.7 6.8	6.8		3.4 3.3	3.4		12.0 12.0	12.0	

Remarks: \* DA: Depth-Averaged

\*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at I2 - Mid-Flood Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
27-Oct-08	Fine	Calm	17:40	Surface	1	26.5 26.4	26.5	7.8 7.7	7.8	31.1 31.1	31.1	97.5 95.7	96.6	6.7 6.6	6.7	6.6	2.8 2.9	2.9	3.1	13.0 13.0	13.0	13.8	
				Middle	4.5	26.2 26.2	26.2	7.6 7.9	7.8	31.2 31.2	31.2	91.7 89.8	90.8	6.5 6.5	6.5		3.1 3.0	3.1		3.0 3.0	13.0 13.0		13.0
				Bottom	8	26.1 26.1	26.1	7.7 7.8	7.8	31.3 31.3	31.3	88.8 88.5	88.7	6.5 6.6	6.6		3.4 3.3	3.4		3.4 3.3	16.0 15.0		15.5
29-Oct-08	Fine	Calm	18:06	Surface	1	26.8 26.8	26.8	7.5 7.5	7.5	31.3 31.2	31.3	93.6 91.4	92.5	6.7 6.6	6.7	6.6	2.8 3.0	2.9	3.1	10.0 10.0	10.0	12.7	
				Middle	4.5	26.6 26.6	26.6	7.4 7.5	7.5	31.3 31.3	31.3	87.1 85.5	86.3	6.5 6.5	6.5		3.1 3.1	3.1		3.1 3.1	13.0 13.0		13.0
				Bottom	8	26.5 26.5	26.5	7.5 7.5	7.5	31.4 31.4	31.4	84.7 84.5	84.6	6.5 6.5	6.5		3.2 3.3	3.3		3.2 3.3	15.0 15.0		15.0
31-Oct-08	Sunny	Calm	14:02	Surface	1	26.8 26.8	26.8	8.2 8.2	8.2	31.2 31.2	31.2	101.3 98.2	99.8	6.8 6.6	6.7	6.6	4.1 4.2	4.2	4.2	13.0 13.0	13.0	13.3	
				Middle	4.5	26.7 26.7	26.7	7.8 7.9	7.9	31.6 31.6	31.6	93.2 92.4	92.8	6.4 6.4	6.4		4.0 4.0	4.0		4.0 4.0	14.0 14.0		14.0
				Bottom	8	26.6 26.6	26.6	8.1 7.7	7.9	31.8 31.8	31.8	92.1 92.0	92.1	6.4 6.4	6.4		4.2 4.3	4.3		4.2 4.3	13.0 13.0		13.0

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake A - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	14:00	Surface	1	27.6 28.0	27.8	8.8 7.8	8.3	27.6 27.4	27.5	132.1 131.2	131.7	9.4 9.4	9.4	8.8	2.1 2.2	2.2	2.6	8.0 8.0	8.0	10.3
				Middle	5	26.9 26.7	26.8	8.5 8.6	8.6	27.4 28.0	27.7	123.9 104.6	114.3	8.8 7.4	8.1		2.3 2.2	2.3		9.0 9.0	9.0	
				Bottom	9	26.2 26.0	26.1	8.0 8.0	8.0	29.1 29.4	29.3	76.9 75.8	76.4	6.2 6.2	6.2		3.2 3.1	3.2		14.0 14.0	14.0	
4-Oct-08	Cloudy	Calm	14:55	Surface	1	27.7 27.9	27.8	8.7 7.8	8.3	27.4 27.3	27.4	122.0 121.4	121.7	8.2 8.2	8.2	8.2	2.1 2.3	2.2	2.5	12.0 12.0	12.0	10.2
				Middle	5	27.0 26.7	26.9	8.3 8.8	8.6	27.6 27.8	27.7	124.0 104.8	114.4	8.7 7.6	8.2		2.1 2.3	2.2		10.0 10.0	10.0	
				Bottom	9	26.2 25.8	26.0	7.8 8.0	7.9	29.1 29.4	29.3	80.0 80.9	80.5	6.0 6.1	6.1		3.1 3.2	3.2		8.0 9.0	8.5	
6-Oct-08	Cloudy	Calm	17:55	Surface	1	25.6 25.6	25.6	8.2 7.2	7.7	30.2 30.1	30.2	92.2 89.3	90.8	7.0 6.8	6.9	6.6	1.1 1.0	1.1	1.5	8.0 8.0	8.0	11.0
				Middle	5	25.4 25.5	25.5	7.8 8.0	7.9	30.3 30.3	30.3	81.6 81.6	81.6	6.3 6.3	6.3		1.3 1.4	1.4		13.0 13.0	13.0	
				Bottom	9	25.0 25.0	25.0	7.4 7.4	7.4	31.0 31.0	31.0	77.6 76.8	77.2	6.1 6.1	6.1		1.8 1.9	1.9		12.0 12.0	12.0	
8-Oct-08	Sunny	Calm	08:29	Surface	1	25.7 25.7	25.7	8.3 8.2	8.3	31.5 31.5	31.5	87.5 87.7	87.6	6.6 6.6	6.6	6.6	1.6 1.7	1.7	1.8	11.0 11.0	11.0	11.2
				Middle	5.5	25.5 25.5	25.5	8.3 8.7	8.5	31.5 31.5	31.5	88.5 88.4	88.5	6.5 6.4	6.5		1.7 1.8	1.8		7.0 7.0	7.0	
				Bottom	10	25.3 25.3	25.3	8.2 8.4	8.3	32.0 32.1	32.1	87.2 85.3	86.3	6.4 6.3	6.4		1.9 2.1	2.0		16.0 15.0	15.5	
10-Oct-08	Sunny	Calm	09:23	Surface	1	26.5 26.5	26.5	8.3 7.7	8.0	27.1 27.1	27.1	92.7 94.3	93.5	7.2 7.4	7.3	7.0	0.8 0.9	0.9	1.4	15.0 15.0	15.0	14.5
				Middle	5	26.2 26.2	26.2	8.2 8.5	8.4	28.1 28.2	28.2	85.4 84.3	84.9	6.6 6.5	6.6		1.2 1.3	1.3		10.0 10.0	10.0	
				Bottom	9	25.6 25.6	25.6	7.7 7.8	7.8	28.5 28.5	28.5	85.4 85.3	85.4	6.2 6.2	6.2		1.8 1.9	1.9		19.0 18.0	18.5	
13-Oct-08	Sunny	Calm	11:12	Surface	1	26.1 26.6	26.4	7.9 7.2	7.6	32.6 32.3	32.5	110.7 105.3	108.0	8.1 7.7	7.9	7.7	2.6 2.5	2.6	2.9	8.0 9.0	8.5	10.0
				Middle	5	26.8 26.8	26.8	8.4 8.4	8.4	32.2 32.2	32.2	100.2 99.7	100.0	7.4 7.3	7.4		3.0 2.9	3.0		14.0 13.0	13.5	
				Bottom	9	26.8 26.8	26.8	7.3 8.0	7.7	32.3 32.2	32.3	99.4 99.4	99.4	7.3 7.3	7.3		3.0 2.9	3.0		8.0 8.0	8.0	
15-Oct-08	Sunny	Calm	12:31	Surface	1	27.8 27.8	27.8	8.7 7.5	8.1	27.6 27.4	27.5	112.0 111.3	111.7	7.4 7.3	7.4	6.9	1.9 2.1	2.0	2.5	12.0 12.0	12.0	15.0
				Middle	5	26.8 26.6	26.7	8.4 8.7	8.6	27.6 27.9	27.8	104.1 84.7	94.4	6.9 5.6	6.3		2.3 2.4	2.4		15.0 15.0	15.0	
				Bottom	9	26.0 26.0	26.0	8.0 7.9	8.0	29.1 29.4	29.3	73.8 74.1	74.0	6.0 6.1	6.1		3.1 3.1	3.1		18.0 18.0	18.0	
17-Oct-08	Sunny	Calm	13:50	Surface	1	27.2 27.4	27.3	7.9 7.4	7.7	31.5 31.3	31.4	97.5 96.2	96.9	7.7 7.6	7.7	7.5	2.6 2.6	2.6	2.9	8.0 8.0	8.0	11.7
				Middle	5	27.4 27.4	27.4	8.1 8.0	8.1	31.3 31.3	31.3	90.4 89.8	90.1	7.2 7.1	7.2		2.7 2.8	2.8		11.0 11.0	11.0	
				Bottom	9	27.4 27.4	27.4	7.4 7.9	7.7	31.3 31.3	31.3	89.1 88.3	88.7	7.1 7.0	7.1		3.2 3.3	3.3		16.0 16.0	16.0	
20-Oct-08	Sunny	Calm	16:05	Surface	1	27.7 27.8	27.8	7.6 8.0	7.8	30.9 30.9	30.9	112.9 109.2	111.1	6.6 6.6	6.6	6.5	2.6 2.6	2.6	3.0	8.0 8.0	8.0	12.8
				Middle	5	27.7 27.7	27.7	7.9 7.8	7.9	30.9 30.9	30.9	103.0 102.3	102.7	6.3 6.5	6.4		2.7 2.8	2.8		14.0 14.0	14.0	
				Bottom	9	27.7 27.7	27.7	7.7 8.0	7.9	30.9 30.9	30.9	101.4 100.3	100.9	6.5 6.4	6.5		3.4 3.5	3.5		17.0 16.0	16.5	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake A - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
22-Oct-08	Sunny	Calm	08:06	Surface	1	26.9 26.9	26.9	7.8 7.7	7.8	31.8 31.6	31.7	109.3 104.7	107.0	6.9 6.7	6.8	6.6	2.6 2.5	2.6	2.9	6.0 6.0	6.0	8.2
				Middle	5	26.2 26.2	26.2	7.7 7.8	7.8	31.5 31.6	31.6	99.1 98.5	98.8	6.4 6.4	6.4		2.9 2.8	2.9		9.0 9.0	9.0	
				Bottom	9	26.2 26.2	26.2	7.7 7.7	7.7	31.6 31.6	31.6	97.9 97.3	97.6	6.4 6.4	6.4		3.2 3.2	3.2		9.0 10.0	9.5	
24-Oct-08	Sunny	Calm	09:44	Surface	1	27.4 27.4	27.4	8.1 7.3	7.7	31.4 31.2	31.3	101.1 96.9	99.0	7.0 6.9	7.0	6.9	2.6 2.6	2.6	2.9	11.0 11.0	11.0	11.7
				Middle	5	27.0 27.0	27.0	7.8 8.2	8.0	31.2 31.2	31.2	91.0 90.4	90.7	6.6 6.7	6.7		2.8 2.8	2.8		13.0 13.0	13.0	
				Bottom	9	26.9 26.9	26.9	7.4 7.5	7.5	31.2 31.2	31.2	89.6 88.8	89.2	6.7 6.7	6.7		3.3 3.4	3.4		11.0 11.0	11.0	
27-Oct-08	Sunny	Calm	11:18	Surface	1	26.5 26.6	26.6	8.5 7.7	8.1	31.0 31.0	31.0	112.0 108.0	110.0	6.7 6.6	6.7	6.6	2.6 2.6	2.6	2.9	12.0 13.0	12.5	10.2
				Middle	5	26.4 26.3	26.4	8.2 8.6	8.4	31.0 31.1	31.1	102.0 101.3	101.7	6.3 6.5	6.4		2.7 2.8	2.8		9.0 9.0	9.0	
				Bottom	9	26.3 26.3	26.3	7.8 7.9	7.9	31.1 31.1	31.1	100.5 99.5	100.0	6.4 6.4	6.4		3.4 3.4	3.4		9.0 9.0	9.0	
29-Oct-08	Sunny	Calm	12:28	Surface	1	27.0 27.0	27.0	7.9 7.8	7.9	31.2 31.1	31.2	106.5 102.4	104.5	6.7 6.6	6.7	6.6	2.6 2.6	2.6	2.9	16.0 16.0	16.0	14.3
				Middle	5	26.7 26.7	26.7	8.1 8.2	8.2	31.1 31.1	31.1	96.5 95.8	96.2	6.3 6.4	6.4		2.7 2.8	2.8		14.0 14.0	14.0	
				Bottom	9	26.6 26.6	26.6	7.6 8.0	7.8	31.1 31.1	31.1	95.0 94.1	94.6	6.4 6.4	6.4		3.4 3.4	3.4		13.0 13.0	13.0	
31-Oct-08	Sunny	Calm	08:13	Surface	1	26.5 26.8	26.7	8.1 8.2	8.2	31.9 31.7	31.8	108.6 103.8	106.2	6.9 6.7	6.8	6.6	3.3 3.5	3.4	3.8	12.0 11.0	11.5	14.2
				Middle	5	26.7 26.7	26.7	8.3 8.3	8.3	31.7 31.7	31.7	98.3 97.7	98.0	6.4 6.4	6.4		3.8 3.8	3.8		13.0 13.0	13.0	
				Bottom	9	26.7 26.7	26.7	8.0 8.0	8.0	31.7 31.7	31.7	97.2 96.7	97.0	6.4 6.3	6.4		4.1 4.1	4.1		18.0 18.0	18.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher



### Water Quality Monitoring Results at Intake A - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	08:22	Surface	1	27.2 27.1	27.2	7.9 8.0	8.0	27.4 27.4	27.4	99.8 102.1	101.0	7.2 7.5	7.4	7.1	2.2 2.3	2.3	2.7	5.0 6.0	5.5	11.5
				Middle	5	26.5 26.4	26.5	8.2 8.0	8.1	28.6 28.7	28.7	98.5 88.9	93.7	7.1 6.5	6.8		2.5 2.6	2.6		8.0 8.0	8.0	
				Bottom	9	26.0 25.9	26.0	8.4 8.4	8.4	29.2 29.6	29.4	74.9 75.8	75.4	6.0 6.1	6.1		3.0 3.2	3.1		21.0 21.0	21.0	
4-Oct-08	Cloudy	Calm	09:47	Surface	1	27.1 27.0	27.1	7.8 8.0	7.9	27.3 27.3	27.3	99.9 102.0	101.0	7.3 7.5	7.4	7.2	2.1 2.2	2.2	2.7	11.0 11.0	11.0	8.8
				Middle	5	26.4 26.3	26.4	8.0 8.0	8.0	28.4 28.6	28.5	98.5 89.0	93.8	7.2 6.7	7.0		2.4 2.7	2.6		8.0 8.0	8.0	
				Bottom	9	26.2 25.8	26.0	8.4 8.4	8.4	29.3 29.4	29.4	76.9 77.4	77.2	6.1 6.2	6.2		3.1 3.2	3.2		7.0 8.0	7.5	
6-Oct-08	Cloudy	Calm	08:52	Surface	1	25.3 25.2	25.3	7.4 7.5	7.5	30.5 30.8	30.7	79.5 79.4	79.5	6.4 6.4	6.4	7.0	1.7 1.9	1.8	1.8	10.0 10.0	10.0	11.2
				Middle	5	26.0 25.9	26.0	7.7 7.5	7.6	28.5 28.5	28.5	102.5 98.7	100.6	7.7 7.4	7.6		1.4 1.4	1.4		11.0 11.0	11.0	
				Bottom	9	25.3 25.2	25.3	8.0 7.9	8.0	29.9 30.0	30.0	81.1 81.1	81.1	6.2 6.2	6.2		2.1 2.1	2.1		11.0 11.0	11.0	
10-Oct-08	Sunny	Calm	16:48	Surface	1	27.3 27.3	27.3	7.7 7.9	7.8	29.9 29.9	29.9	99.1 97.9	98.5	7.2 7.1	7.2	7.1	1.2 1.1	1.2	1.7	17.0 17.0	17.0	14.2
				Middle	5	27.0 27.0	27.0	8.2 7.9	8.1	30.1 30.1	30.1	95.3 94.2	94.8	6.9 6.8	6.9		1.8 1.8	1.8		12.0 12.0	12.0	
				Bottom	9	26.3 26.3	26.3	8.2 8.4	8.3	30.7 30.7	30.7	86.0 84.6	85.3	6.3 6.2	6.3		2.0 2.1	2.1		13.0 14.0	13.5	
13-Oct-08	Sunny	Calm	18:33	Surface	1	26.7 26.7	26.7	7.7 7.5	7.6	32.2 32.2	32.2	98.2 99.5	98.9	7.2 7.3	7.3	7.2	3.4 3.4	3.4	3.4	11.0 11.0	11.0	11.8
				Middle	5	26.8 26.8	26.8	7.8 7.7	7.8	32.3 32.3	32.3	96.1 96.1	96.1	7.1 7.1	7.1		3.4 3.4	3.4		7.0 8.0	7.5	
				Bottom	9	26.8 26.8	26.8	7.8 8.3	8.1	32.3 32.3	32.3	95.2 94.8	95.0	7.0 7.0	7.0		3.5 3.5	3.5		17.0 17.0	17.0	
15-Oct-08	Fine	Calm	18:14	Surface	1	27.1 27.0	27.1	7.9 8.0	8.0	27.4 27.4	27.4	99.9 101.9	100.9	7.3 7.4	7.4	7.2	2.2 2.4	2.3	2.7	11.0 11.0	11.0	14.0
				Middle	5	26.4 26.2	26.3	8.2 7.9	8.1	28.4 28.5	28.5	98.3 88.9	93.6	7.2 6.6	6.9		2.6 2.7	2.7		12.0 12.0	12.0	
				Bottom	9	26.0 25.7	25.9	8.4 8.4	8.4	29.3 29.6	29.5	75.1 79.9	77.5	6.1 6.6	6.4		3.0 3.3	3.2		19.0 19.0	19.0	
17-Oct-08	Sunny	Calm	08:26	Surface	1	27.6 27.6	27.6	7.4 7.5	7.5	31.3 31.3	31.3	90.9 91.3	91.1	7.2 7.2	7.2	7.1	3.0 3.1	3.1	3.3	14.0 13.0	13.5	11.8
				Middle	5	27.4 27.4	27.4	7.9 7.8	7.9	31.4 31.4	31.4	87.2 86.3	86.8	7.0 6.9	7.0		3.1 3.2	3.2		12.0 12.0	12.0	
				Bottom	9	27.3 27.3	27.3	7.7 7.9	7.8	31.4 31.3	31.4	84.9 83.8	84.4	6.8 6.7	6.8		3.4 3.6	3.5		10.0 10.0	10.0	
20-Oct-08	Sunny	Calm	11:56	Surface	1	28.0 28.0	28.0	7.4 7.7	7.6	30.8 30.9	30.9	104.7 104.7	104.7	6.4 6.8	6.6	6.7	2.8 2.9	2.9	3.2	6.0 7.0	6.5	6.5
				Middle	5	27.7 27.8	27.8	7.9 7.7	7.8	30.9 30.9	30.9	100.3 98.9	99.6	6.8 6.6	6.7		3.0 3.1	3.1		8.0 8.0	8.0	
				Bottom	9	27.6 27.6	27.6	7.3 7.6	7.5	30.9 30.9	30.9	97.2 95.8	96.5	6.3 6.4	6.4		3.4 3.7	3.6		5.0 5.0	5.0	
24-Oct-08	Sunny	Calm	16:37	Surface	1	27.3 27.4	27.4	7.3 7.5	7.4	31.5 31.5	31.5	88.9 89.6	89.3	6.6 6.9	6.8	6.8	2.7 2.8	2.8	3.1	12.0 12.0	12.0	12.0
				Middle	5	27.3 27.3	27.3	7.6 7.6	7.6	31.6 31.6	31.6	85.7 85.0	85.4	6.7 6.7	6.7		3.1 3.2	3.2		13.0 13.0	13.0	
				Bottom	9	27.2 27.2	27.2	7.9 8.0	8.0	31.6 31.6	31.6	83.7 82.8	83.3	6.4 6.5	6.5		3.4 3.4	3.4		11.0 11.0	11.0	

Remarks: \* DA: Depth-Averaged

\*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake A - Mid-Flood Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
27-Oct-08	Fine	Calm	17:24	Surface	1	26.7	26.7	7.7	7.9	31.2	31.2	101.8	102.0	6.3	6.5	6.6	2.7	2.8	3.1	12.0	12.0	11.7
				Middle	5	26.5	26.5	8.1	8.0	31.2	31.2	98.0	97.5	6.6	6.6		3.0	3.1		15.0	15.0	
				Bottom	9	26.4	26.4	8.3	8.4	31.2	31.2	95.4	94.9	6.2	6.3		6.3	3.4		3.5	8.0	
29-Oct-08	Fine	Calm	17:53	Surface	1	27.0	27.0	7.6	7.6	31.4	31.4	95.3	95.6	6.3	6.5	6.5	2.7	2.8	3.1	15.0	15.0	13.5
				Middle	5	26.9	26.9	7.7	7.7	31.4	31.4	91.8	91.4	6.5	6.5		3.0	3.1		15.0	15.5	
				Bottom	9	26.8	26.8	7.7	7.8	31.4	31.4	89.5	89.0	6.2	6.2		6.2	3.4		3.5	10.0	
31-Oct-08	Sunny	Calm	13:53	Surface	1	26.9	26.9	7.9	8.0	31.8	31.8	96.7	97.2	6.3	6.4	6.4	3.9	4.0	4.3	17.0	17.0	10.8
				Middle	5	26.8	26.8	8.1	8.0	31.8	31.8	93.9	93.7	6.3	6.3		4.1	4.3		7.0	7.5	
				Bottom	9	26.8	26.8	7.9	8.1	31.9	31.9	92.3	92.0	6.1	6.1		6.1	4.5		4.5	8.0	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake B - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	14:23	Surface	1	27.0 27.0	27.0	7.4 7.9	7.7	28.1 28.1	28.1	100.7 97.2	99.0	7.4 7.0	7.2	7.1	2.7 2.8	2.8	3.6	7.0 8.0	7.5	7.2
				Middle	6	26.7 26.4	26.6	8.3 7.7	8.0	28.6 28.5	28.6	96.6 95.3	96.0	7.0 7.0	7.0		3.3 3.9	3.6		7.0 7.0	7.0	
				Bottom	11	26.5 26.2	26.4	8.2 8.5	8.4	28.7 28.9	28.8	81.7 81.7	81.7	6.4 6.4	6.4		6.4 6.4	6.4		4.3 4.6	4.5	
4-Oct-08	Cloudy	Calm	15:18	Surface	1	27.0 27.0	27.0	7.4 7.9	7.7	28.1 28.1	28.1	100.7 97.0	98.9	7.4 7.1	7.3	7.2	2.8 2.9	2.9	3.6	13.0 13.0	13.0	10.3
				Middle	6	26.6 26.6	26.6	8.5 7.7	8.1	28.4 28.4	28.4	96.7 95.1	95.9	6.8 7.1	7.0		3.4 3.8	3.6		8.0 8.0	8.0	
				Bottom	11	26.4 26.4	26.4	8.3 8.5	8.4	28.7 28.9	28.8	82.8 82.6	82.7	6.3 6.3	6.3		6.3 6.3	6.3		4.3 4.5	4.4	
6-Oct-08	Cloudy	Calm	18:14	Surface	1	25.8 25.8	25.8	7.0 7.4	7.2	29.5 29.5	29.5	90.5 89.2	89.9	6.9 6.8	6.9	6.5	1.7 1.6	1.7	1.7	9.0 9.0	9.0	8.5
				Middle	6	25.3 25.3	25.3	7.8 7.1	7.5	30.5 30.4	30.5	78.4 78.5	78.5	6.0 6.1	6.1		1.6 1.6	1.6		9.0 9.0	9.0	
				Bottom	11	24.9 24.9	24.9	7.1 7.9	7.9	31.1 31.1	31.1	77.1 78.2	77.7	6.0 6.1	6.1		6.1 6.1	6.1		1.8 1.7	1.8	
8-Oct-08	Sunny	Calm	09:04	Surface	1	25.4 25.4	25.4	8.1 8.0	8.1	32.0 32.0	32.0	88.2 89.5	88.9	6.6 6.7	6.7	6.7	1.7 1.6	1.7	1.7	6.0 7.0	6.5	10.8
				Middle	5	25.3 25.4	25.4	8.1 7.9	8.0	32.1 32.6	32.4	91.2 86.5	88.9	7.0 6.2	6.6		1.5 1.7	1.6		13.0 13.0	13.0	
				Bottom	9	25.0 25.0	25.0	8.2 8.4	8.3	33.1 32.6	32.9	88.0 88.2	88.1	6.3 6.4	6.4		6.4 6.4	6.4		1.8 1.8	1.8	
10-Oct-08	Sunny	Calm	09:53	Surface	1	26.6 26.6	26.6	7.6 7.7	7.7	29.9 30.1	30.0	97.9 98.1	98.0	7.1 7.1	7.1	7.1	2.1 2.0	2.1	2.5	18.0 18.0	18.0	14.7
				Middle	6	26.1 26.1	26.1	8.3 7.8	8.1	30.1 30.7	30.4	99.2 91.0	95.1	7.3 6.8	7.1		2.4 2.4	2.4		14.0 14.0	14.0	
				Bottom	11	25.8 25.8	25.8	8.1 8.0	8.1	30.7 29.5	30.1	89.6 86.6	88.1	6.7 6.5	6.6		6.6 6.6	6.6		2.9 2.8	2.9	
13-Oct-08	Sunny	Calm	11:40	Surface	1	26.4 26.5	26.5	8.2 7.6	7.9	32.2 32.1	32.2	117.0 110.8	113.9	8.5 8.1	8.3	7.8	3.8 3.7	3.8	4.1	12.0 12.0	12.0	10.0
				Middle	1	26.8 26.8	26.8	7.9 8.1	8.0	32.3 32.3	32.3	97.2 97.0	97.1	7.2 7.1	7.2		3.9 4.0	4.0		8.0 8.0	8.0	
				Bottom	1	26.8 26.8	26.8	7.7 7.9	7.8	32.3 32.3	32.3	95.7 95.6	95.7	7.1 7.1	7.1		7.1 7.1	7.1		4.4 4.4	4.4	
15-Oct-08	Sunny	Calm	12:54	Surface	1	26.9 26.8	26.9	7.5 7.8	7.7	28.1 27.9	28.0	100.6 97.2	98.9	7.3 7.1	7.2	7.1	2.7 2.8	2.8	3.7	16.0 16.0	16.0	15.0
				Middle	6	26.5 26.4	26.5	8.4 7.5	8.0	28.4 28.4	28.4	96.7 95.2	96.0	7.0 7.0	7.0		3.5 3.9	3.7		17.0 17.0	17.0	
				Bottom	11	26.4 26.2	26.3	8.2 8.2	8.2	28.9 29.1	29.0	82.9 82.7	82.8	6.1 6.1	6.1		6.1 6.1	6.1		4.4 4.5	4.5	
17-Oct-08	Sunny	Calm	14:27	Surface	1	27.0 27.0	27.0	7.5 7.5	7.5	31.3 31.2	31.3	99.9 93.8	96.9	7.9 7.4	7.7	7.2	3.2 3.3	3.3	4.0	8.0 8.0	8.0	11.7
				Middle	6	26.8 26.8	26.8	7.7 7.5	7.6	31.5 31.5	31.5	80.3 79.6	80.0	6.6 6.5	6.6		3.8 3.9	3.9		11.0 11.0	11.0	
				Bottom	11	26.7 26.7	26.7	7.6 8.0	7.8	31.6 31.6	31.6	77.2 76.9	77.1	6.4 6.3	6.4		6.4 6.4	6.4		4.6 4.7	4.7	
20-Oct-08	Sunny	Calm	16:33	Surface	1	27.2 27.3	27.3	7.5 7.4	7.5	30.8 30.7	30.8	108.9 102.8	105.9	6.4 6.3	6.4	6.5	3.1 3.4	3.3	4.0	10.0 10.0	10.0	13.3
				Middle	6	26.8 26.8	26.8	7.5 7.6	7.6	31.1 31.1	31.1	89.3 88.4	88.9	6.4 6.5	6.5		3.8 4.1	4.0		13.0 13.0	13.0	
				Bottom	11	26.7 26.7	26.7	7.6 7.8	7.7	31.2 31.3	31.3	85.5 85.0	85.3	6.4 6.3	6.4		6.4 6.4	6.4		4.8 4.8	4.8	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake B - Mid-Ebb Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
22-Oct-08	Sunny	Calm	08:34	Surface	1	26.8 26.9	26.9	7.8 7.8	7.8	31.5 31.4	31.5	110.4 104.3	107.4	6.9 6.7	6.8	6.6	3.2 3.8	3.5	4.0	12.0 12.0	12.0	12.8
				Middle	6	26.8 26.8	26.8	7.4 7.5	7.5	31.7 31.7	31.7	90.7 90.2	90.5	6.3 6.3	6.3		3.9 4.0	4.0		10.0 10.0	10.0	
				Bottom	11	26.7 26.7	26.7	7.7 7.7	7.7	31.8 31.8	31.8	88.1 87.8	88.0	6.2 6.2	6.2		4.6 4.6	4.6		17.0 16.0	16.5	
24-Oct-08	Sunny	Calm	09:13	Surface	1	27.0 27.1	27.1	7.1 7.4	7.3	31.1 31.1	31.1	99.6 93.5	96.6	7.0 6.8	6.9	6.8	2.9 3.1	3.0	3.6	10.0 10.0	10.0	11.8
				Middle	6	26.8 26.8	26.8	7.9 7.2	7.6	31.4 31.4	31.4	80.0 79.3	79.7	6.6 6.7	6.7		3.4 3.6	3.5		12.0 12.0	12.0	
				Bottom	11	26.7 26.7	26.7	7.7 7.8	7.8	31.5 31.5	31.5	76.8 76.4	76.6	6.6 6.5	6.6		4.1 4.2	4.2		14.0 13.0	13.5	
27-Oct-08	Sunny	Calm	11:50	Surface	1	26.1 26.2	26.2	7.5 7.8	7.7	31.0 30.9	31.0	109.2 103.1	106.2	6.5 6.4	6.5	6.5	3.0 3.2	3.1	3.8	10.0 10.0	10.0	11.3
				Middle	6	25.8 25.8	25.8	8.4 7.7	8.1	31.2 31.2	31.2	89.6 88.8	89.2	6.3 6.5	6.4		3.6 3.8	3.7		11.0 11.0	11.0	
				Bottom	11	25.7 25.7	25.7	8.2 8.2	8.2	31.4 31.4	31.4	86.1 85.7	85.9	6.4 6.3	6.4		4.4 4.5	4.5		13.0 13.0	13.0	
29-Oct-08	Sunny	Calm	13:05	Surface	1	26.6 26.6	26.6	8.1 7.9	8.0	31.1 31.0	31.1	104.4 98.3	101.4	6.6 6.5	6.6	6.5	2.9 3.0	3.0	3.4	12.0 12.0	12.0	13.7
				Middle	6	26.3 26.3	26.3	7.7 8.3	8.0	31.3 31.3	31.3	84.8 84.0	84.4	6.3 6.5	6.4		3.3 3.4	3.4		13.0 13.0	13.0	
				Bottom	11	26.2 26.2	26.2	7.6 7.7	7.7	31.4 31.5	31.5	81.4 81.0	81.2	6.3 6.2	6.3		3.9 3.8	3.9		16.0 16.0	16.0	
31-Oct-08	Sunny	Calm	08:55	Surface	1	26.5 26.6	26.6	7.6 7.8	7.7	31.4 31.5	31.5	110.7 104.2	107.5	7.1 6.8	7.0	6.7	4.1 4.6	4.4	4.7	8.0 8.0	8.0	13.2
				Middle	6	26.5 26.5	26.5	7.9 7.9	7.9	31.8 31.8	31.8	91.0 90.5	90.8	6.2 6.3	6.3		4.6 4.7	4.7		16.0 16.0	16.0	
				Bottom	11	26.5 26.5	26.5	8.0 7.9	8.0	31.9 31.9	31.9	88.5 88.3	88.4	6.2 6.1	6.2		5.0 5.1	5.1		16.0 15.0	15.5	

Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

### Water Quality Monitoring Results at Intake B - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
2-Oct-08	Sunny	Calm	08:43	Surface	1	27.2 27.1	27.2	8.8 8.7	8.8	27.9 28.0	28.0	95.0 101.5	98.3	6.6 7.1	6.9	6.8	2.2 2.2	2.2	3.2	9.0 10.0	9.5	12.5
				Middle	6	26.5 26.3	26.4	8.3 7.9	8.1	28.8 28.6	28.7	93.5 88.3	90.9	6.7 6.6	6.7		3.1 3.1	3.1		13.0 13.0	13.0	
				Bottom	11	26.1 26.1	26.1	7.8 7.8	7.8	29.2 29.3	29.3	76.7 77.6	77.2	6.1 6.2	6.2		4.1 4.4	4.3		15.0 15.0	15.0	
4-Oct-08	Cloudy	Calm	10:08	Surface	1	27.3 27.3	27.3	8.8 8.6	8.7	27.8 28.0	27.9	95.0 101.5	98.3	6.8 7.1	7.0	6.9	2.3 2.3	2.3	3.2	11.0 11.0	11.0	10.0
				Middle	6	26.7 26.2	26.5	8.4 7.7	8.1	28.7 28.6	28.7	93.5 88.3	90.9	6.7 6.7	6.7		3.0 3.1	3.1		11.0 11.0	11.0	
				Bottom	11	26.0 26.2	26.1	8.0 7.6	7.8	29.2 29.2	29.2	75.6 76.7	76.2	6.0 6.1	6.1		4.1 4.1	4.1		8.0 8.0	8.0	
6-Oct-08	Cloudy	Calm	09:10	Surface	1	25.0 25.0	25.0	8.4 8.0	8.2	30.5 30.5	30.5	86.5 86.1	86.3	6.9 6.9	6.9	7.1	1.8 1.7	1.8	2.0	9.0 9.0	9.0	10.8
				Middle	6	26.0 26.0	26.0	7.9 7.3	7.6	28.9 28.9	28.9	94.9 94.4	94.7	7.2 7.1	7.2		2.0 1.9	2.0		11.0 11.0	11.0	
				Bottom	11	25.7 25.6	25.7	7.4 7.2	7.3	29.6 29.7	29.7	87.3 86.3	86.8	6.7 6.6	6.7		2.1 2.1	2.1		15.0 15.0	15.0	
10-Oct-08	Sunny	Calm	17:19	Surface	1	27.3 27.3	27.3	8.8 8.5	8.7	31.7 31.8	31.8	97.2 97.7	97.5	7.2 7.2	7.2	7.2	1.7 1.7	1.7	2.2	11.0 11.0	11.0	14.0
				Middle	6	27.3 27.3	27.3	8.3 7.7	8.0	32.2 33.0	32.6	95.4 95.7	95.6	7.1 7.1	7.1		2.2 2.3	2.3		17.0 17.0	17.0	
				Bottom	11	27.2 27.2	27.2	7.8 7.6	7.7	29.8 29.8	29.8	84.8 83.9	84.4	6.2 6.2	6.2		2.7 2.7	2.7		14.0 14.0	14.0	
13-Oct-08	Sunny	Calm	17:58	Surface	1	26.4 26.5	26.5	8.1 8.0	8.1	32.3 32.3	32.3	108.0 108.0	108.0	7.9 7.9	7.9	7.4	2.7 2.8	2.8	3.2	11.0 11.0	11.0	11.3
				Middle	6	26.8 26.8	26.8	7.7 7.8	7.8	32.2 32.1	32.2	93.1 93.1	93.1	6.9 6.9	6.9		3.3 3.4	3.4		14.0 14.0	14.0	
				Bottom	11	26.8 26.8	26.8	7.9 7.7	7.8	32.0 30.9	31.5	92.7 92.9	92.8	6.9 6.9	6.9		3.3 3.3	3.3		9.0 9.0	9.0	
15-Oct-08	Fine	Calm	18:36	Surface	1	27.3 27.3	27.3	9.0 8.5	8.8	27.9 27.9	27.9	95.0 101.5	98.3	6.7 7.3	7.0	6.8	3.3 2.8	3.1	3.7	3.0 3.0	3.0	11.0
				Middle	6	26.5 26.4	26.5	8.3 7.7	8.0	28.8 28.5	28.7	93.4 88.3	90.9	6.7 6.5	6.6		3.5 3.8	3.7		13.0 13.0	13.0	
				Bottom	11	26.2 26.1	26.2	7.9 7.7	7.8	29.2 29.3	29.3	83.7 81.6	82.7	6.8 6.7	6.8		4.0 4.4	4.2		18.0 16.0	17.0	
17-Oct-08	Sunny	Calm	09:01	Surface	1	26.9 26.8	26.9	7.9 7.8	7.9	31.3 31.4	31.4	84.9 84.7	84.8	6.9 6.9	6.9	6.6	3.1 3.0	3.1	3.6	9.0 10.0	9.5	10.5
				Middle	6	26.8 26.8	26.8	7.6 7.8	7.7	31.3 31.3	31.3	76.0 75.4	75.7	6.3 6.2	6.3		3.6 3.7	3.7		9.0 9.0	9.0	
				Bottom	11	26.7 26.7	26.7	7.9 7.8	7.9	31.3 30.8	31.1	74.3 74.2	74.3	6.2 6.2	6.2		3.9 4.0	4.0		13.0 13.0	13.0	
20-Oct-08	Sunny	Calm	12:30	Surface	1	27.0 27.0	27.0	7.3 7.4	7.4	30.9 30.9	30.9	90.8 90.6	90.7	6.6 6.3	6.5	6.5	2.9 3.1	3.0	3.7	10.0 10.0	10.0	12.2
				Middle	6	26.8 26.9	26.9	7.8 8.1	8.0	30.9 30.9	30.9	84.9 84.0	84.5	6.5 6.5	6.5		3.8 3.9	3.9		13.0 14.0	13.5	
				Bottom	11	26.8 26.8	26.8	7.9 8.3	8.1	31.0 31.0	31.0	82.6 82.3	82.5	6.4 6.4	6.4		4.2 4.3	4.3		13.0 13.0	13.0	
24-Oct-08	Sunny	Calm	16:07	Surface	1	26.7 26.7	26.7	8.4 8.1	8.3	31.6 31.6	31.6	86.9 86.8	86.9	7.1 6.9	7.0	6.8	2.4 2.5	2.5	2.9	8.0 8.0	8.0	10.5
				Middle	6	26.8 26.8	26.8	7.9 7.3	7.6	31.5 31.5	31.5	76.5 76.0	76.3	6.5 6.5	6.5		2.9 3.1	3.0		11.0 10.0	10.5	
				Bottom	11	26.8 26.8	26.8	7.5 7.1	7.3	31.5 31.0	31.3	75.1 75.1	75.1	6.4 6.4	6.4		3.1 3.2	3.2		13.0 13.0	13.0	

Remarks: \* DA: Depth-Averaged


\*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

**Water Quality Monitoring Results at Intake B - Mid-Flood Tide**

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Water Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
27-Oct-08	Fine	Calm	17:59	Surface	1	25.9 25.9	25.9	8.8 8.6	8.7	31.2 31.2	31.2	93.8 93.7	93.8	6.7 6.5	6.6	6.5	2.6 2.8	2.7	3.3	11.0 11.0	11.0	14.0
				Middle	6	25.8 25.8	25.8	8.4 7.7	8.1	31.2 31.2	31.2	85.7 85.0	85.4	6.3 6.3	6.3		3.3 3.5	3.4		16.0 16.0	16.0	
				Bottom	11	25.8 25.8	25.8	7.9 7.6	7.8	31.3 31.0	31.2	83.8 83.7	83.8	6.3 6.3	6.3		3.6 3.7	3.7		15.0 15.0	15.0	
29-Oct-08	Fine	Calm	18:28	Surface	1	26.3 26.3	26.3	7.8 7.8	7.8	31.4 31.4	31.4	90.3 90.2	90.3	6.7 6.6	6.7	6.5	2.5 2.6	2.6	3.1	12.0 12.0	12.0	13.3
				Middle	6	26.3 26.3	26.3	7.6 7.7	7.7	31.4 31.4	31.4	81.1 80.5	80.8	6.2 6.2	6.2		3.1 3.3	3.2		12.0 12.0	12.0	
				Bottom	11	26.3 26.3	26.3	7.7 7.6	7.7	31.4 31.0	31.2	79.4 79.4	79.4	6.2 6.2	6.2		3.3 3.4	3.4		16.0 16.0	16.0	
31-Oct-08	Sunny	Calm	14:35	Surface	1	27.0 26.9	27.0	8.1 8.1	8.1	31.4 31.4	31.4	99.1 99.1	99.1	6.8 6.7	6.8	6.5	3.6 3.7	3.7	4.1	10.0 10.0	10.0	9.3
				Middle	6	26.8 26.8	26.8	8.4 8.2	8.3	31.8 31.8	31.8	87.1 86.8	87.0	6.1 6.1	6.1		4.2 4.3	4.3		9.0 9.0	9.0	
				Bottom	11	26.5 26.5	26.5	8.0 8.3	8.2	31.9 30.9	31.4	86.0 86.1	86.1	6.0 6.1	6.1		4.3 4.4	4.4		9.0 9.0	9.0	



Remarks: \* DA: Depth-Averaged  
 \*\* Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher

## Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

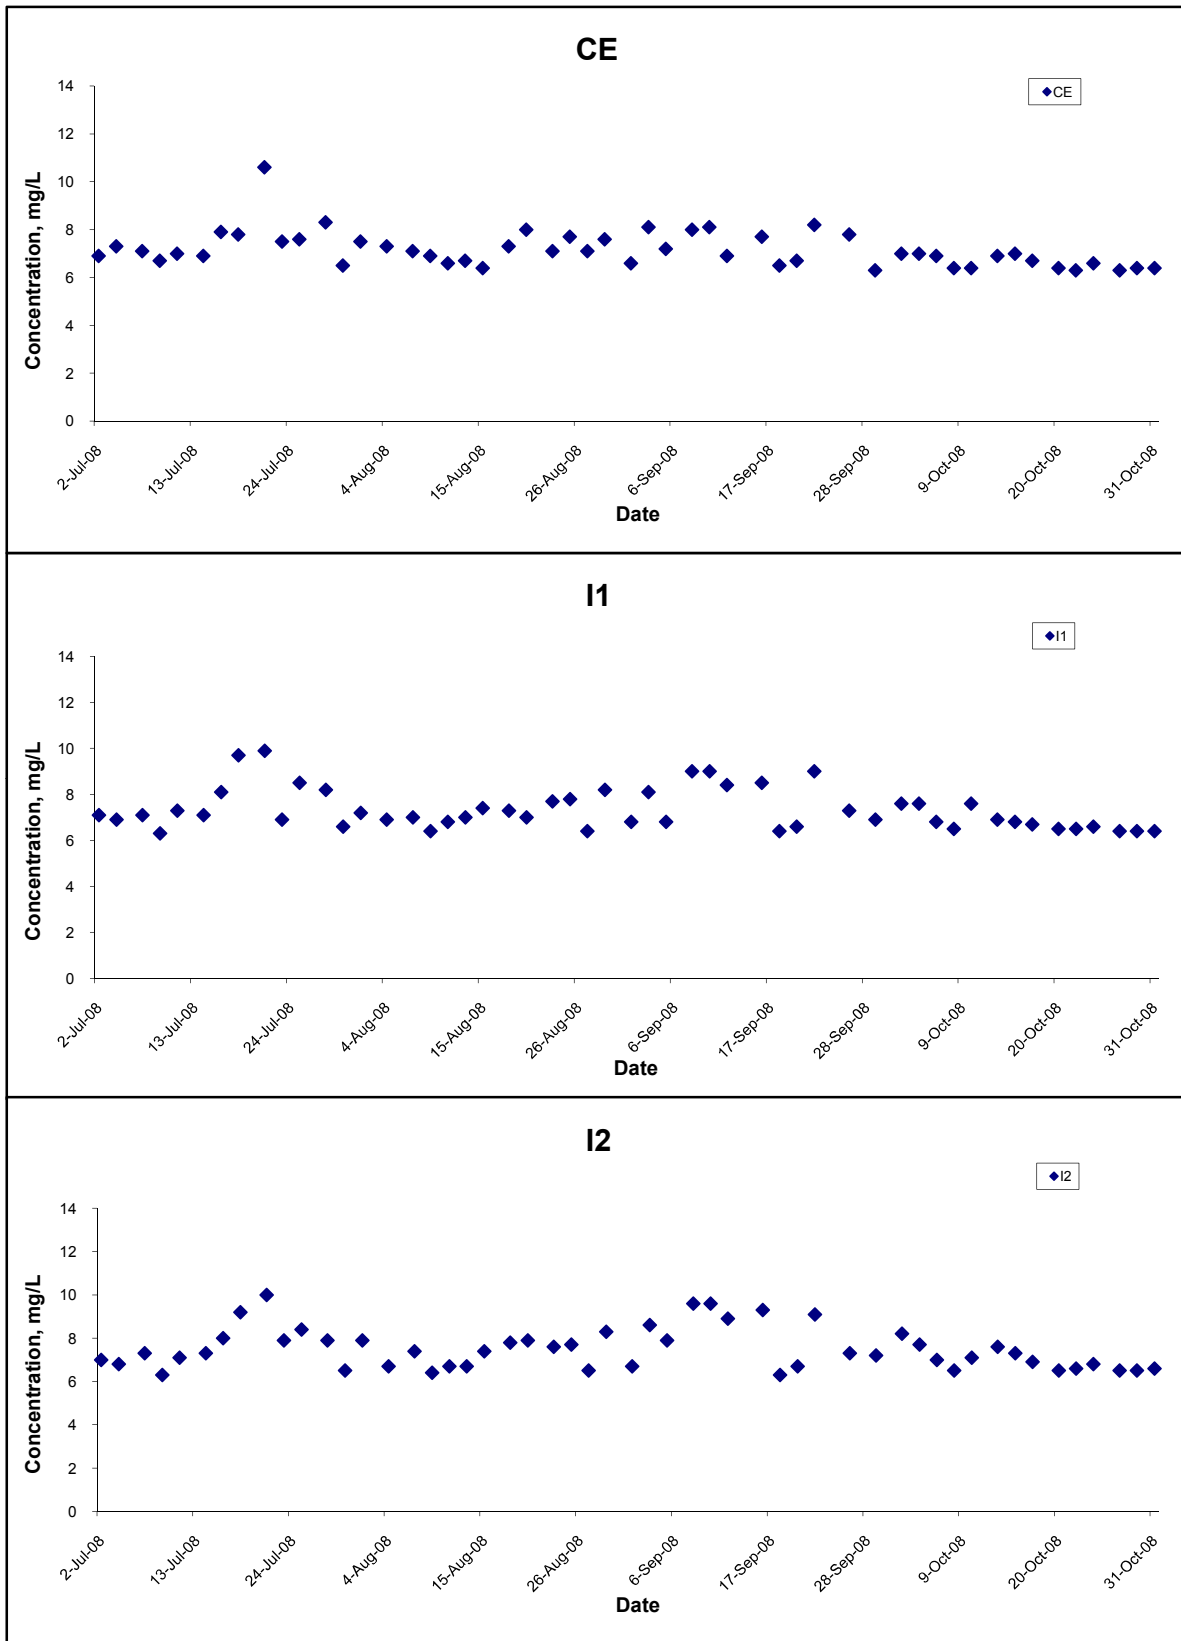

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix H	




## Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

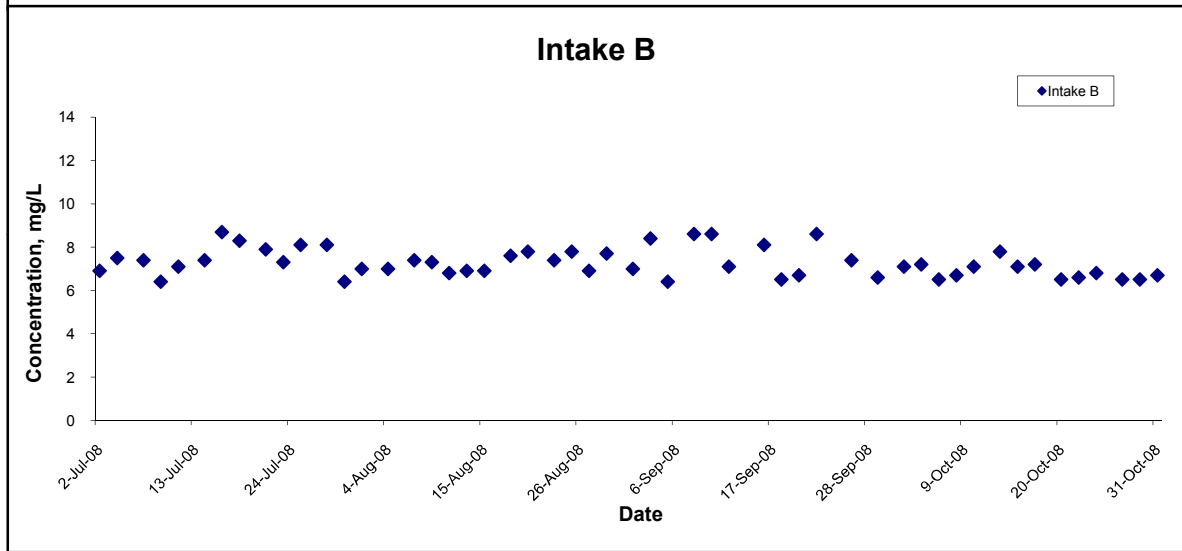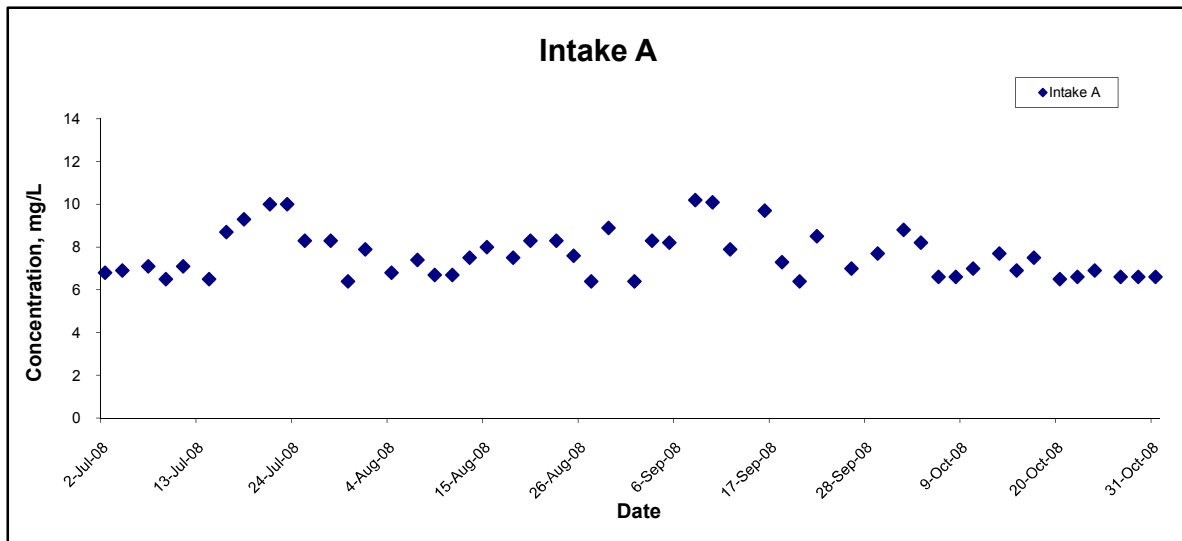

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale	N.T.S	Project No. MA8001	<b>CINOTECH</b>
	Date	Oct 08	Appendix H	





## Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

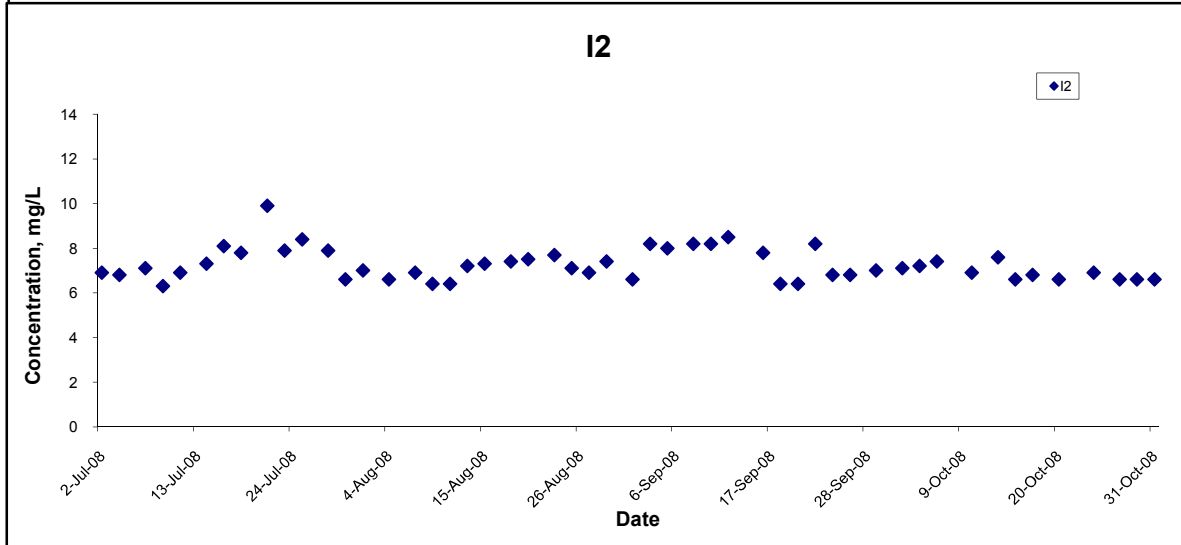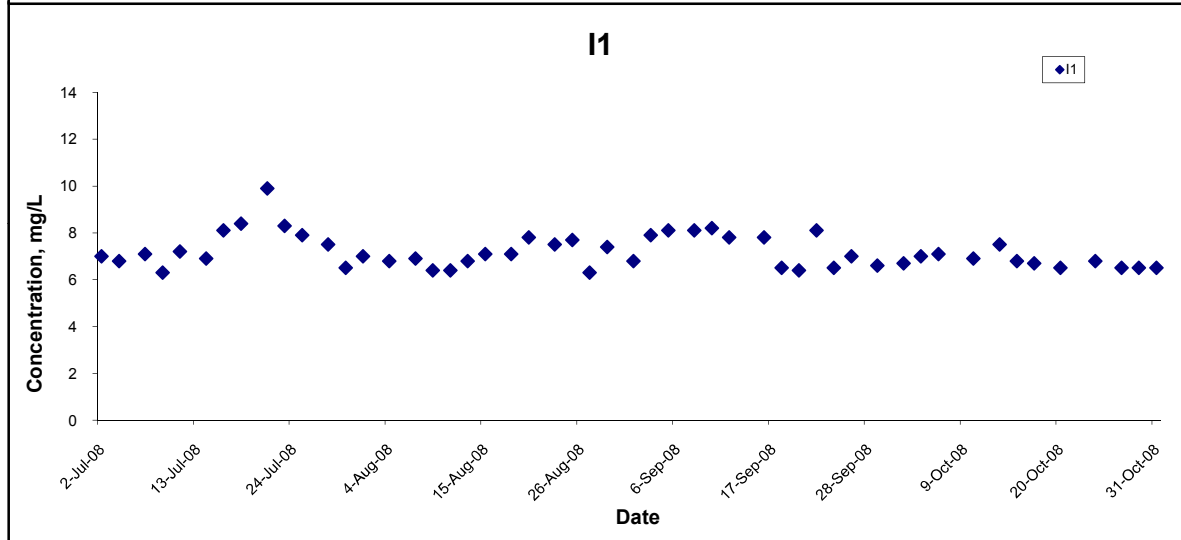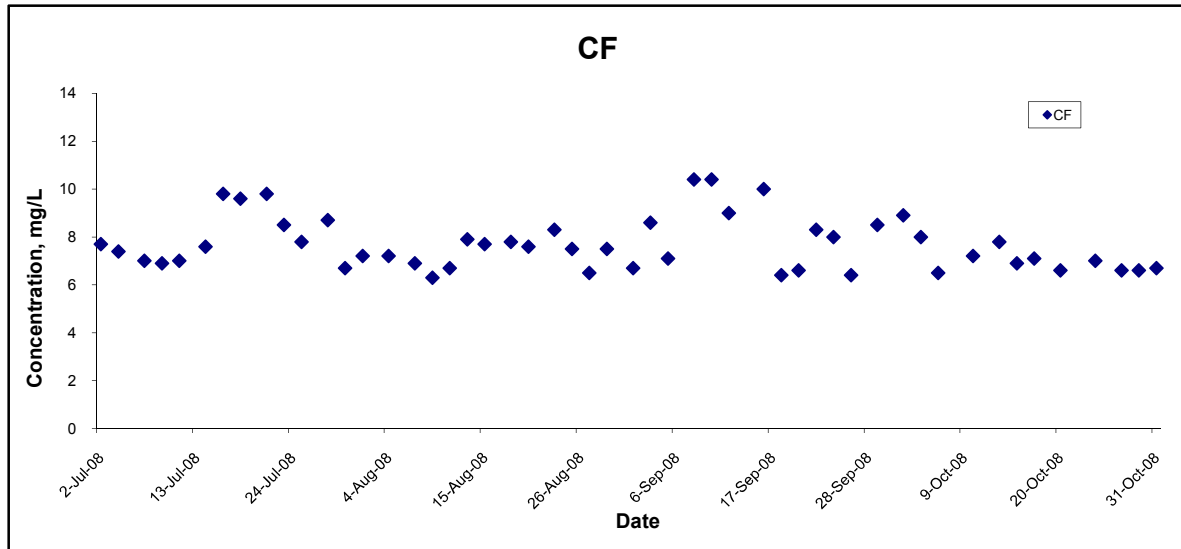




Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

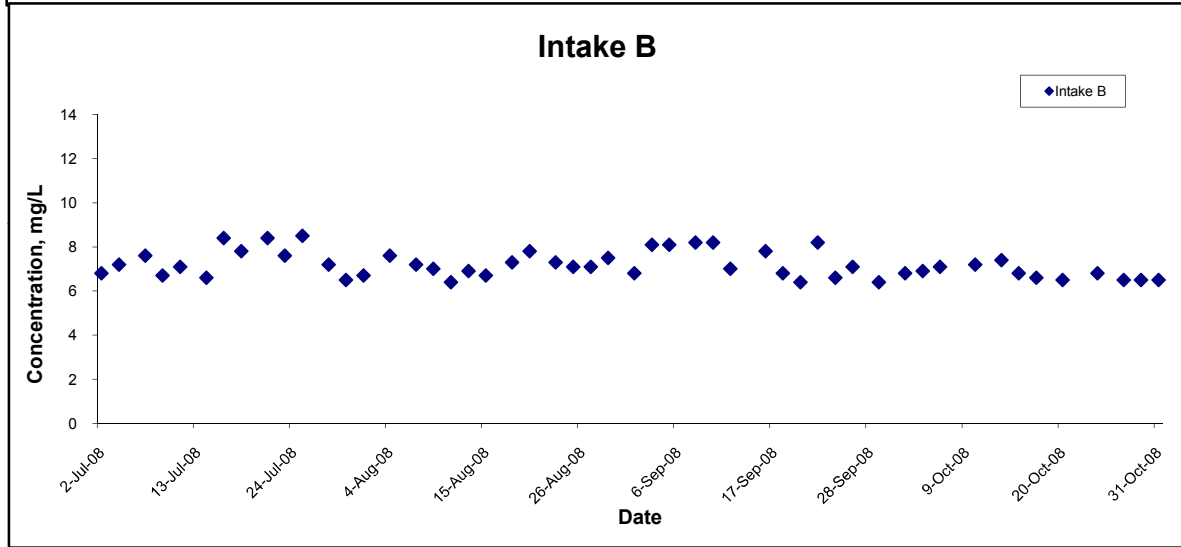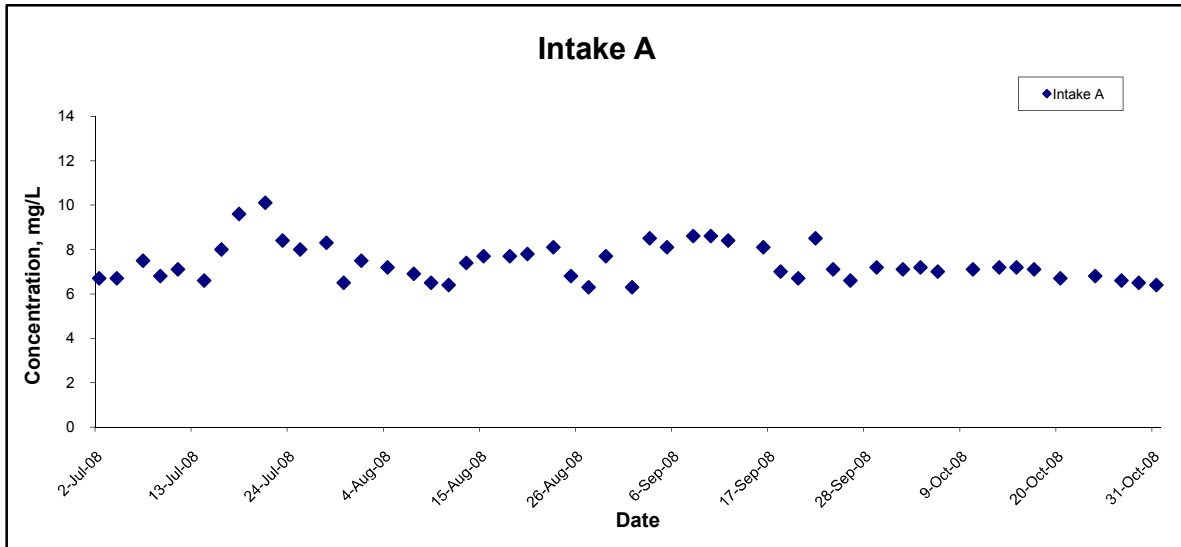



Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Dissolved Oxygen (Bottom) at Mid-Ebb Tide

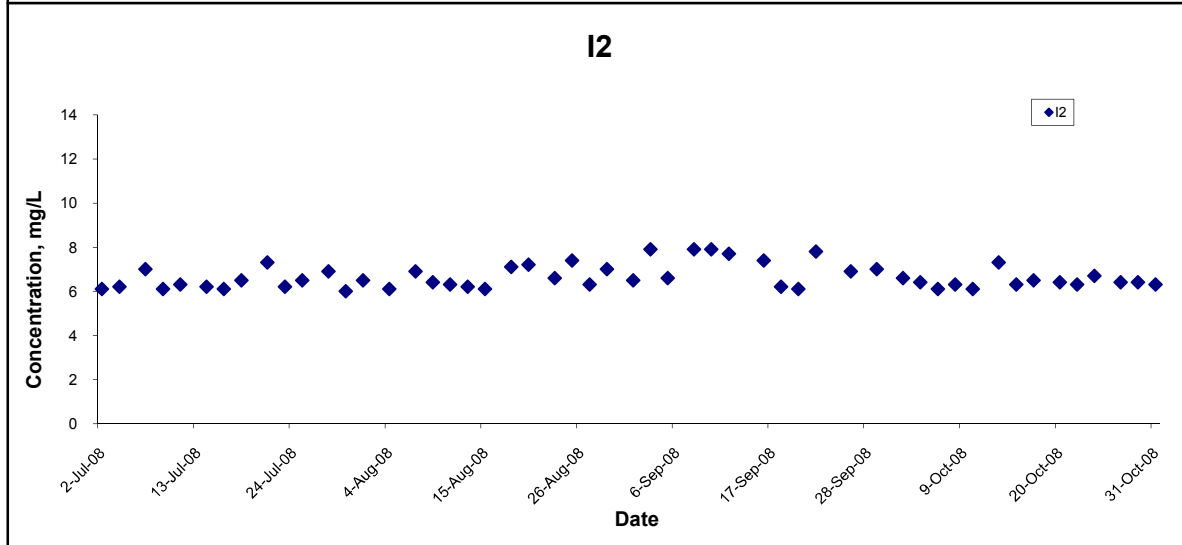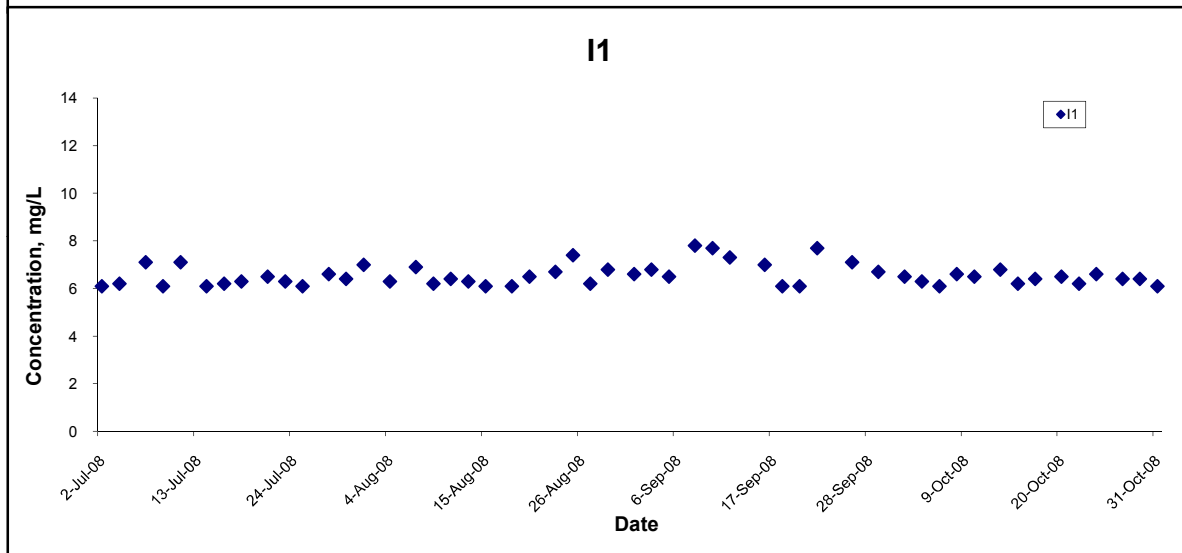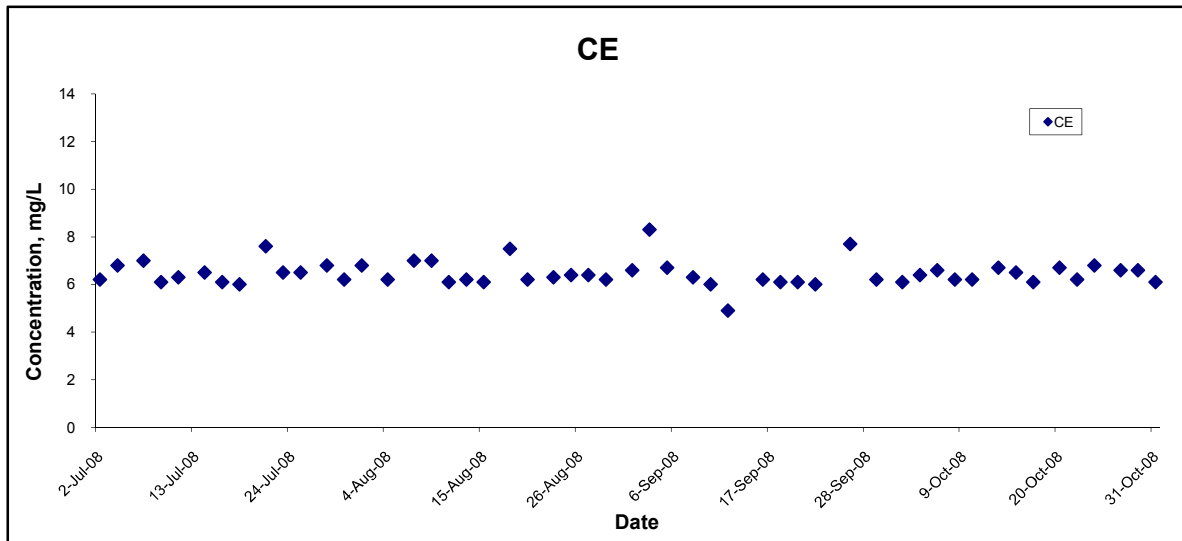




Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix H	

## Dissolved Oxygen (Bottom) at Mid-Ebb Tide

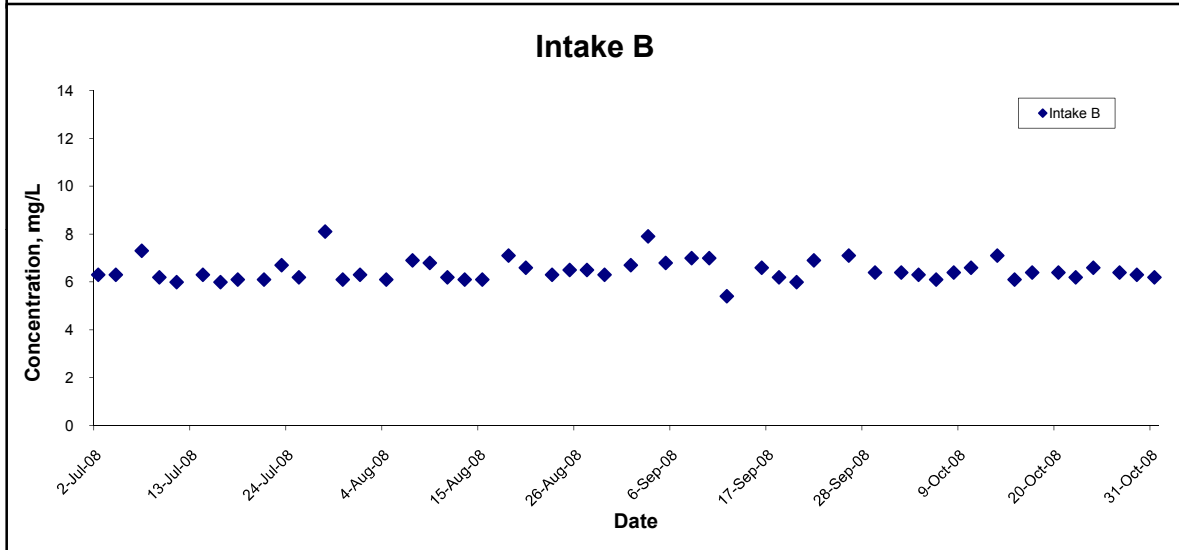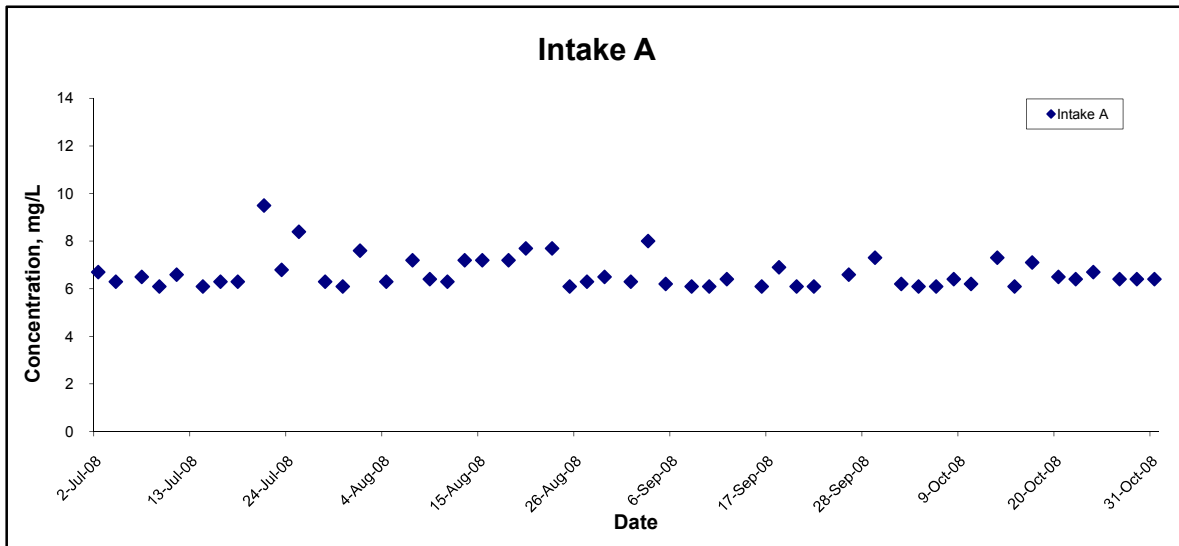



Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Dissolved Oxygen (Bottom) at Mid-Flood Tide

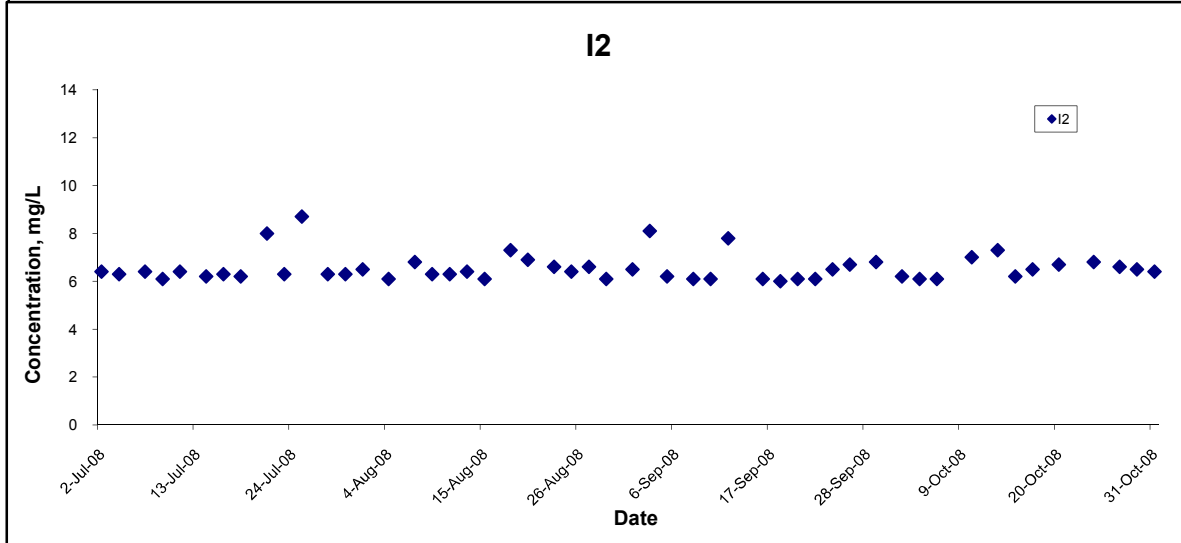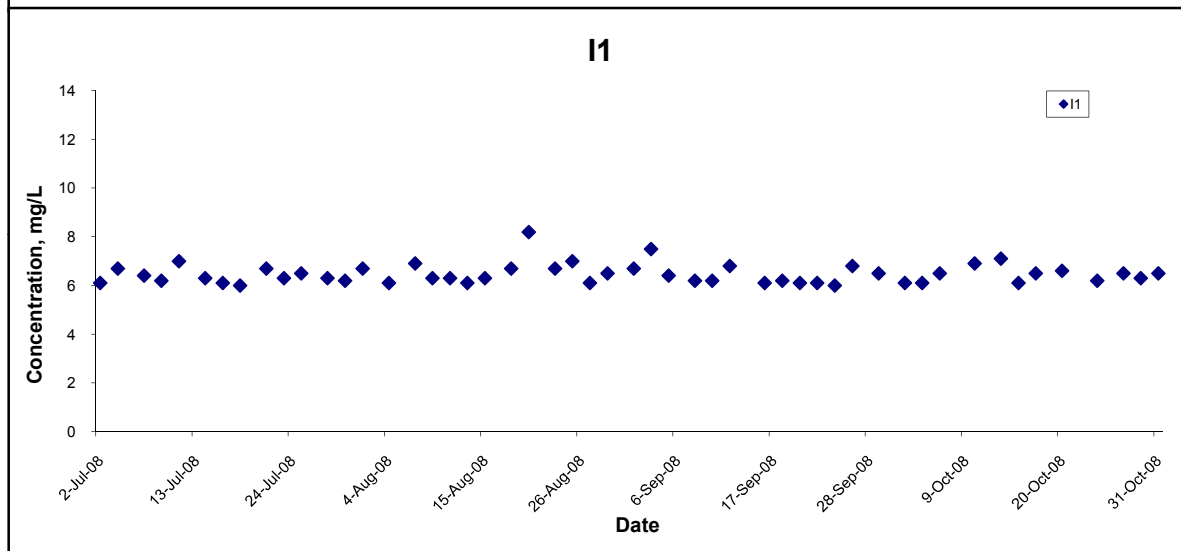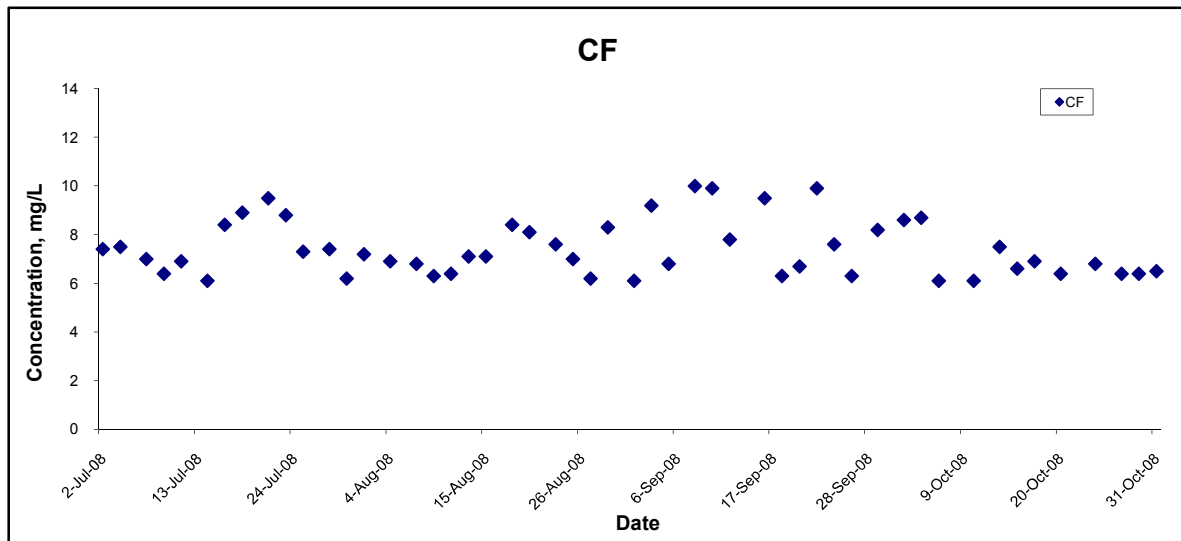


Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Dissolved Oxygen (Bottom) at Mid-Flood Tide

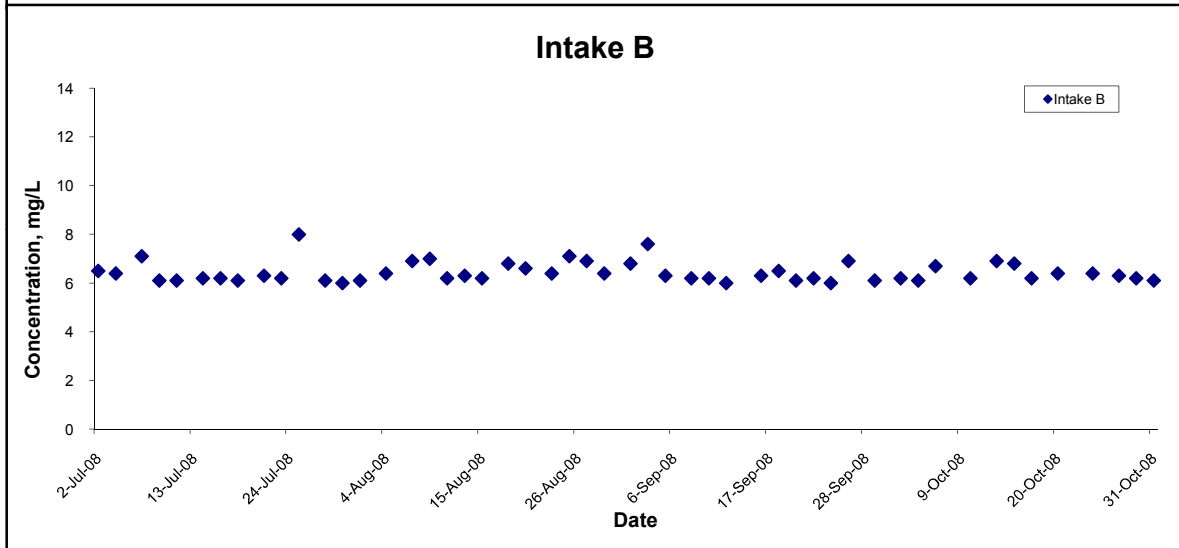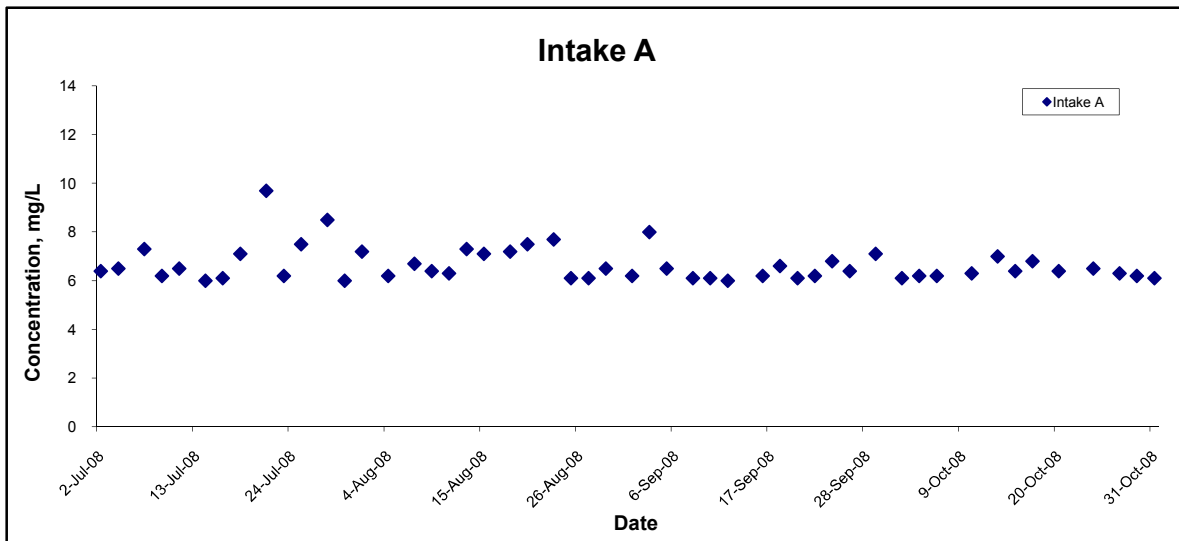


Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Turbidity (Depth-averaged) at Mid-Ebb Tide

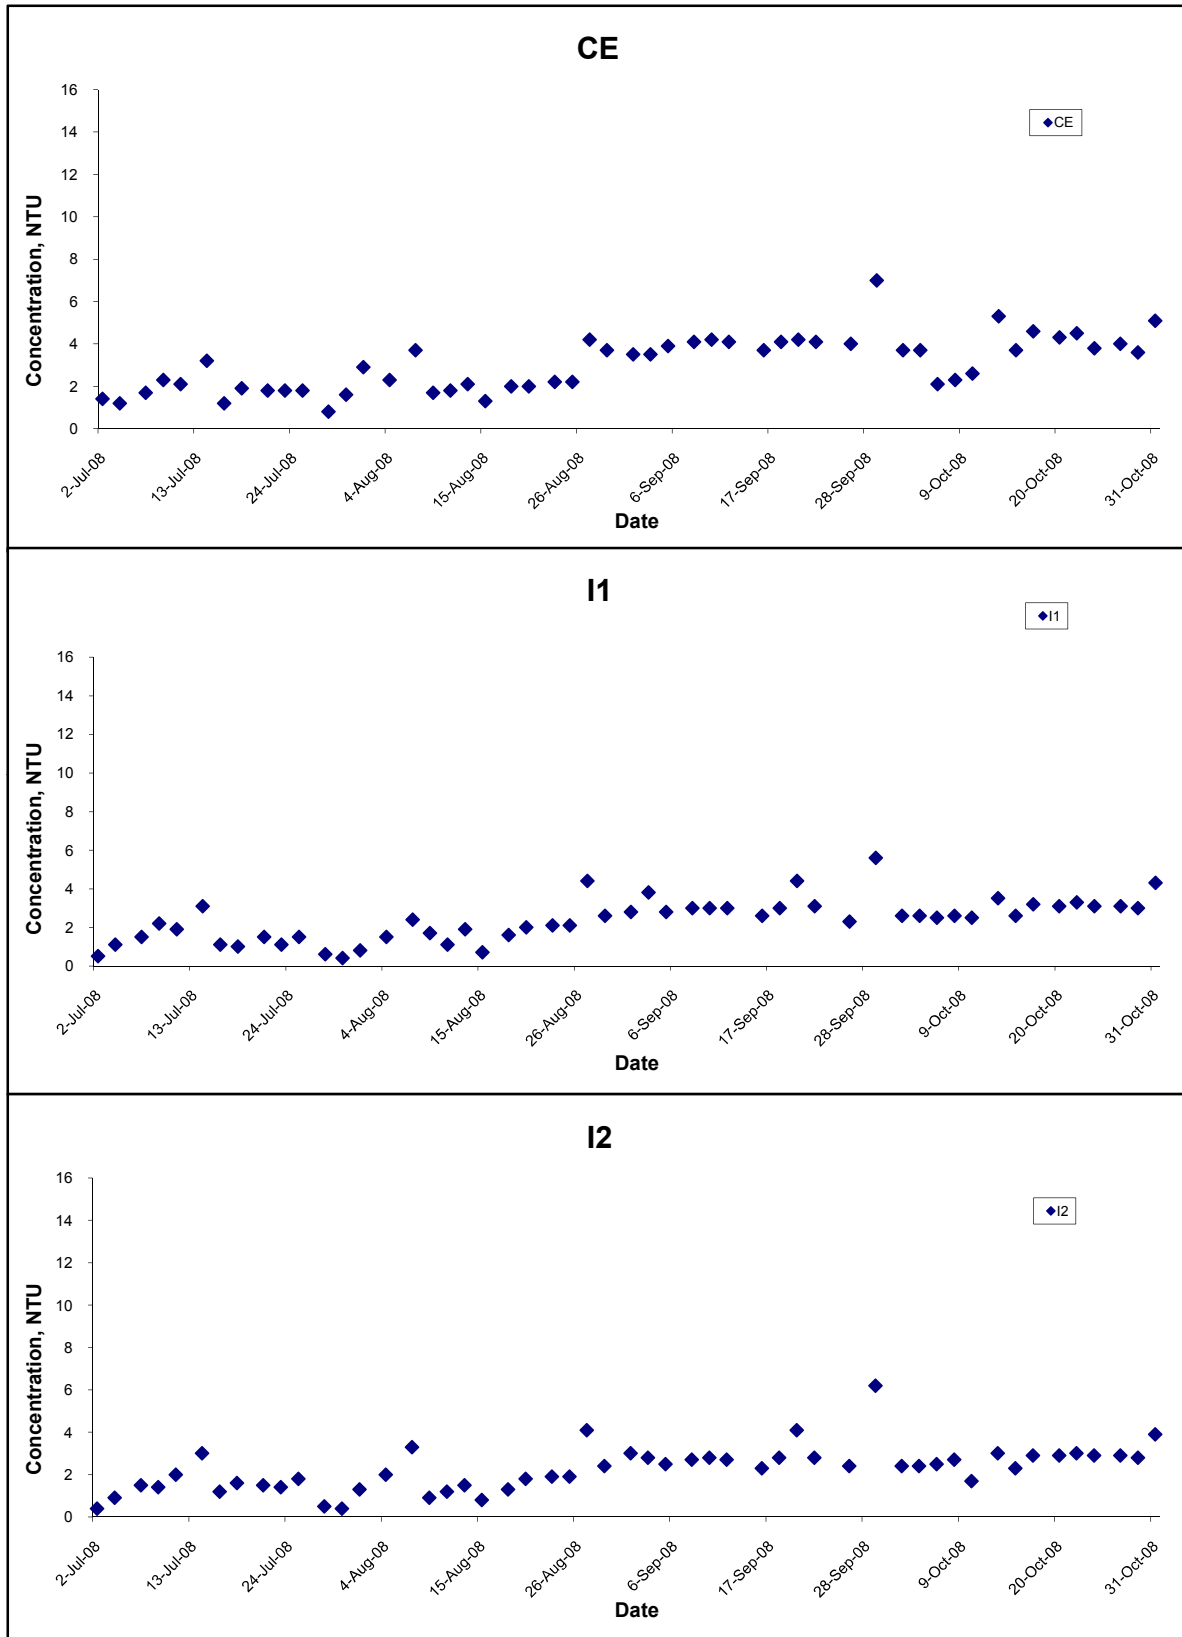

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	




## Turbidity (Depth-averaged) at Mid-Ebb Tide

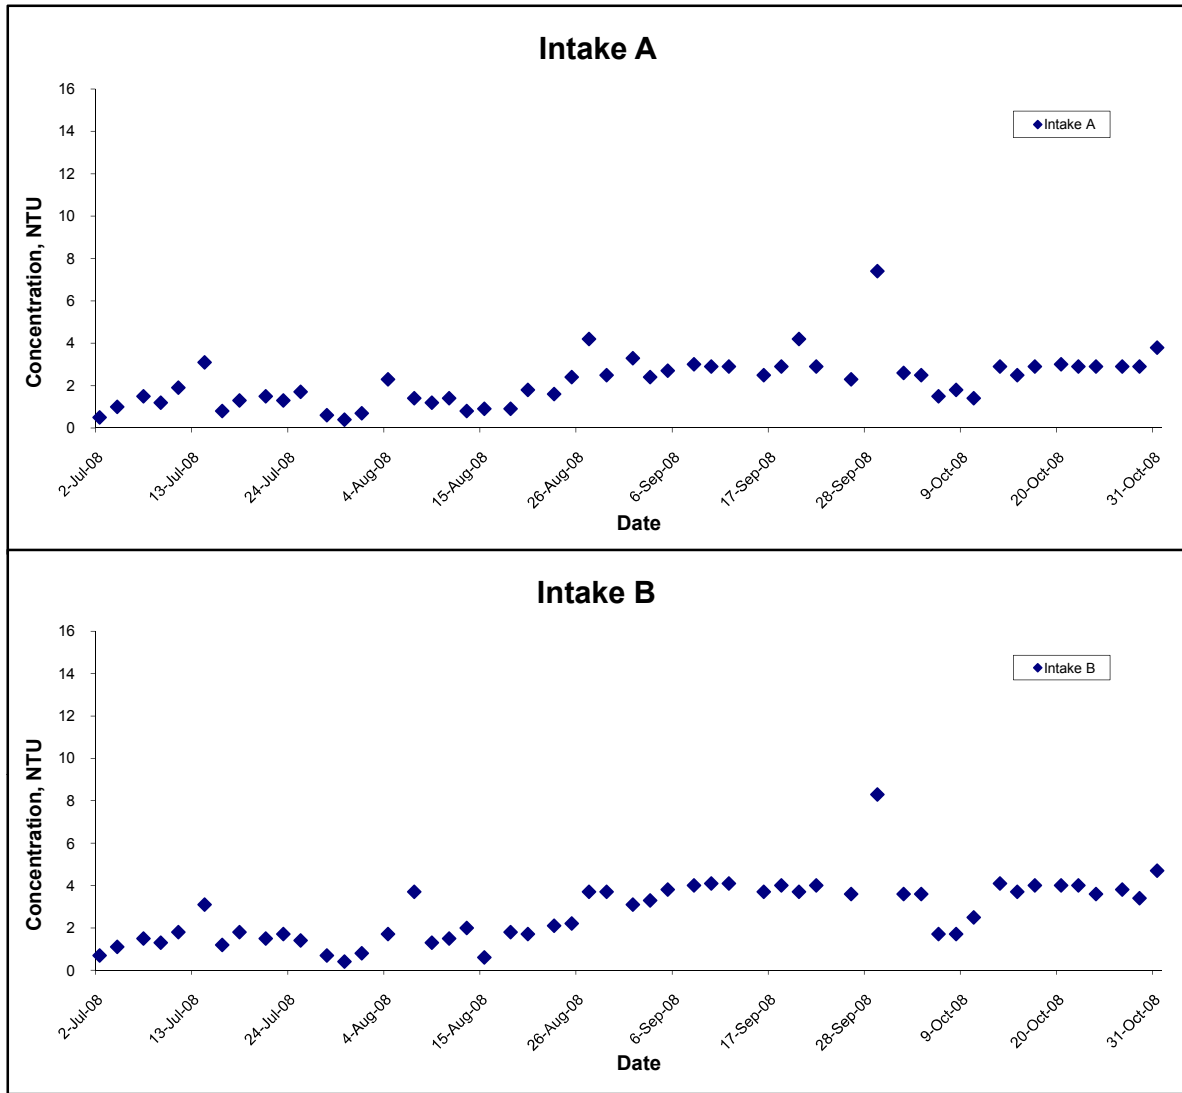

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	<b>CINOTECH</b>
	Date Oct 08	Appendix H	





## Turbidity (Depth-averaged) at Mid-Flood Tide

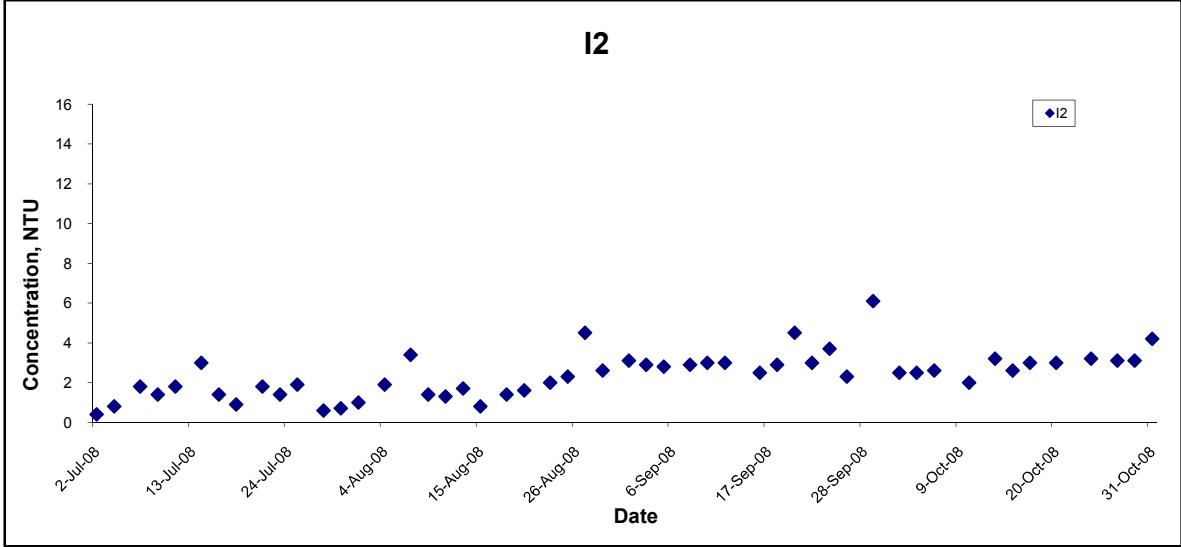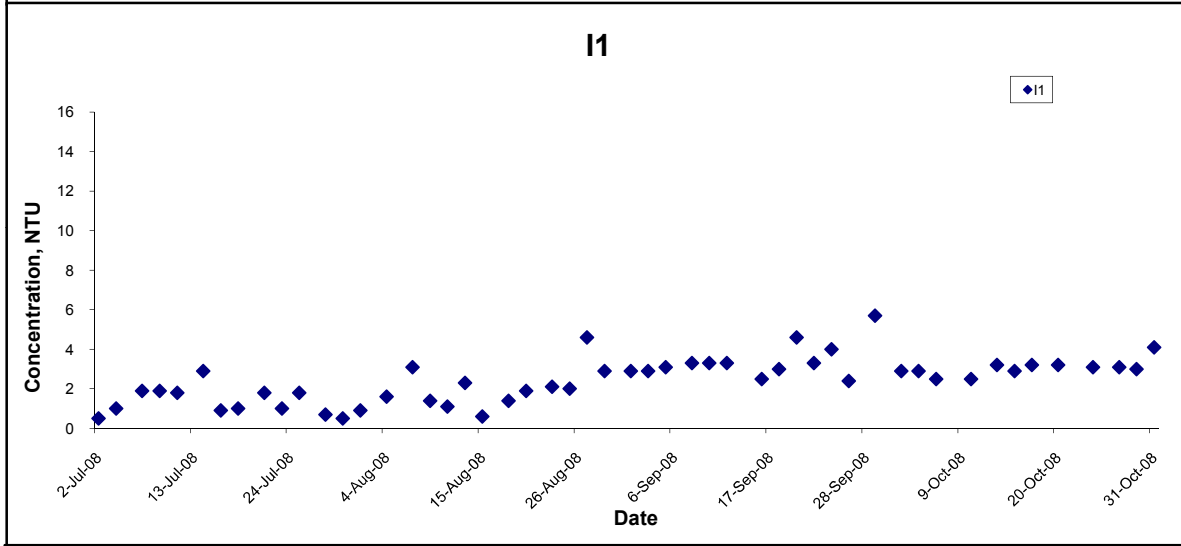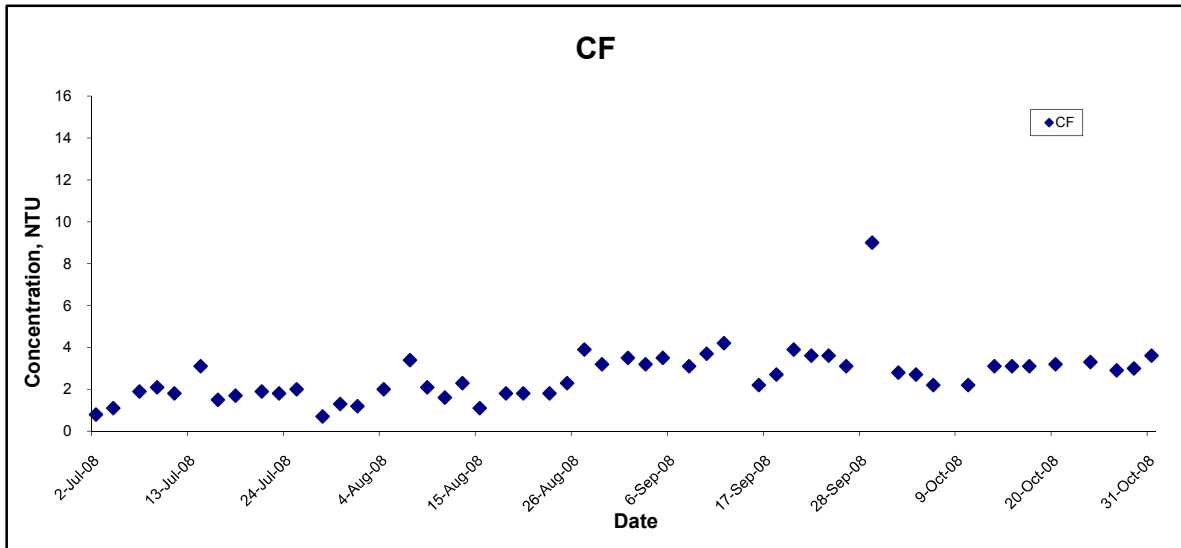




Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix H	

## Turbidity (Depth-averaged) at Mid-Flood Tide

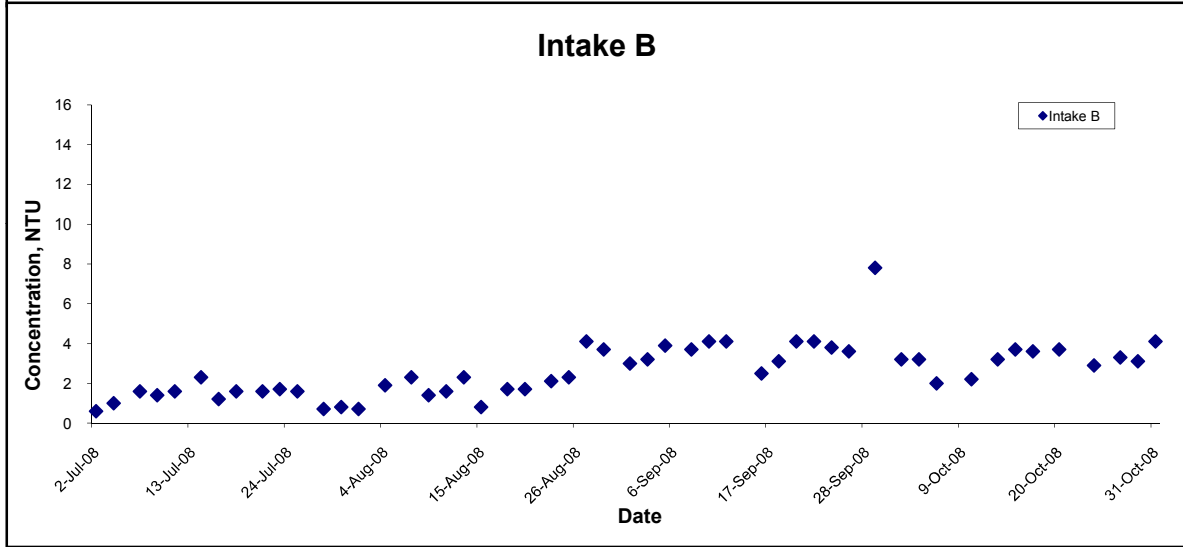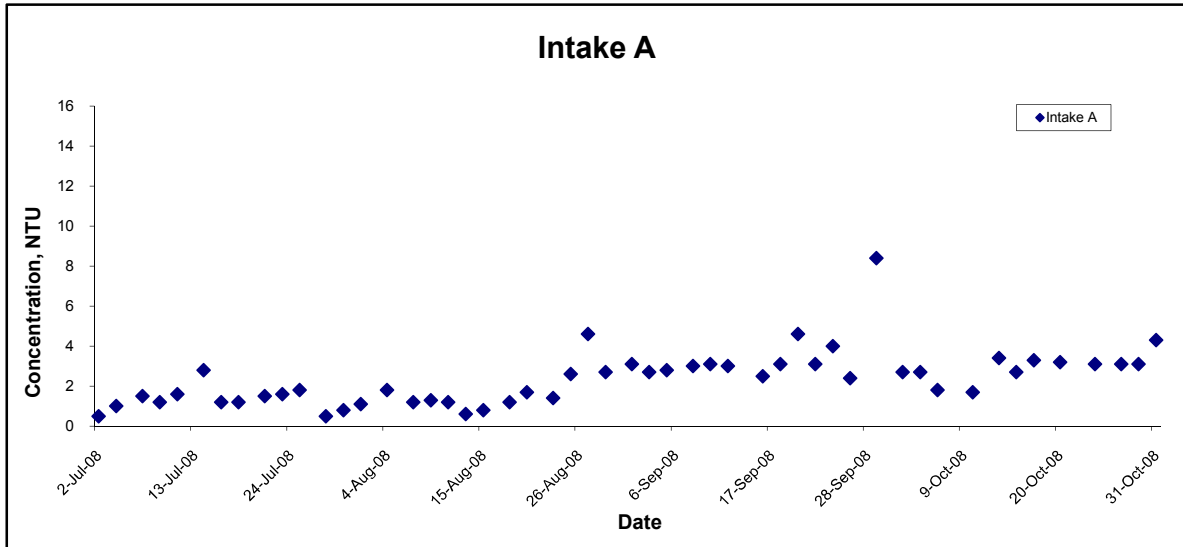



Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix H	

## Suspended Solids (Depth-averaged) at Mid-Ebb Tide

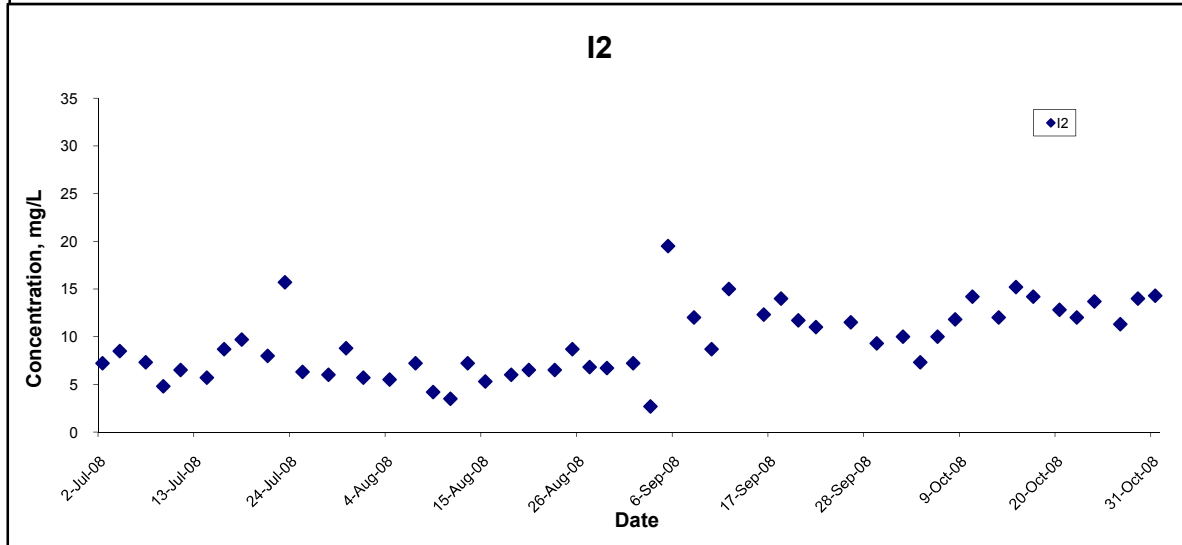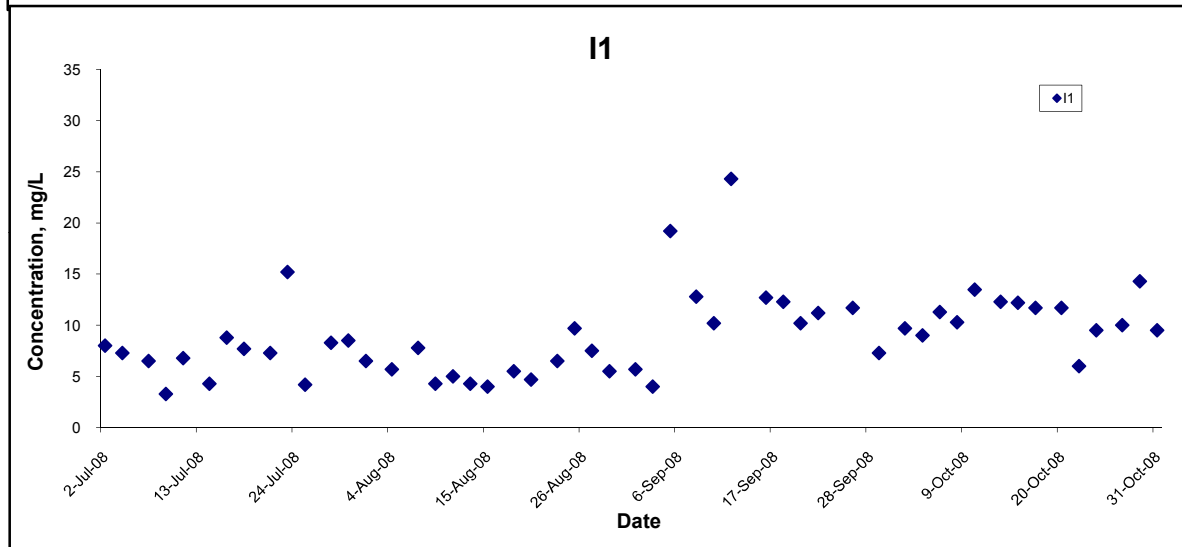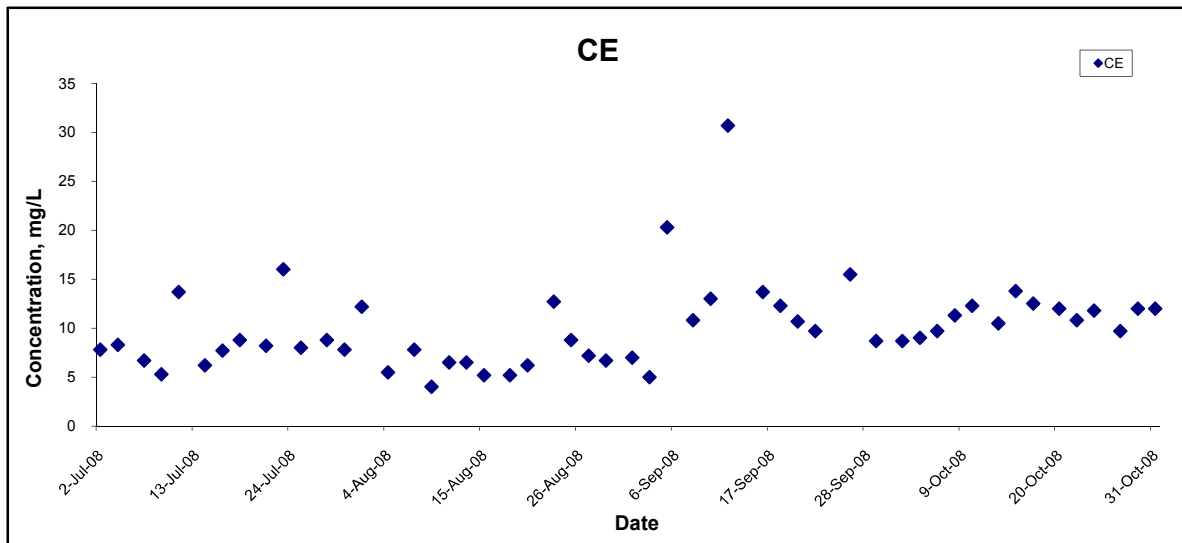


Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	
	Date Oct 08	Appendix H	

## Suspended Solids (Depth-averaged) at Mid-Ebb Tide

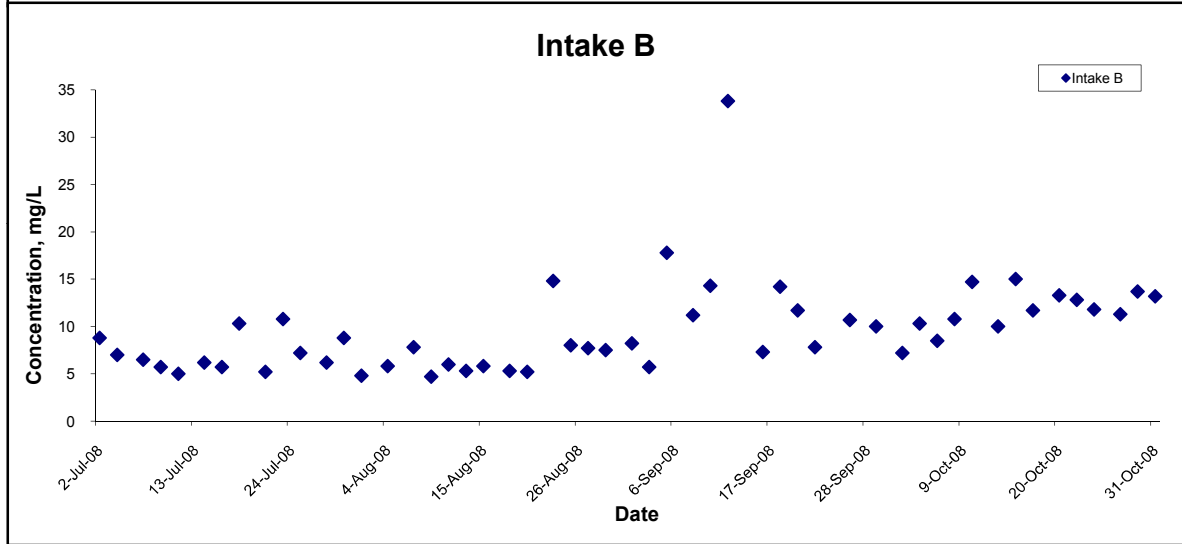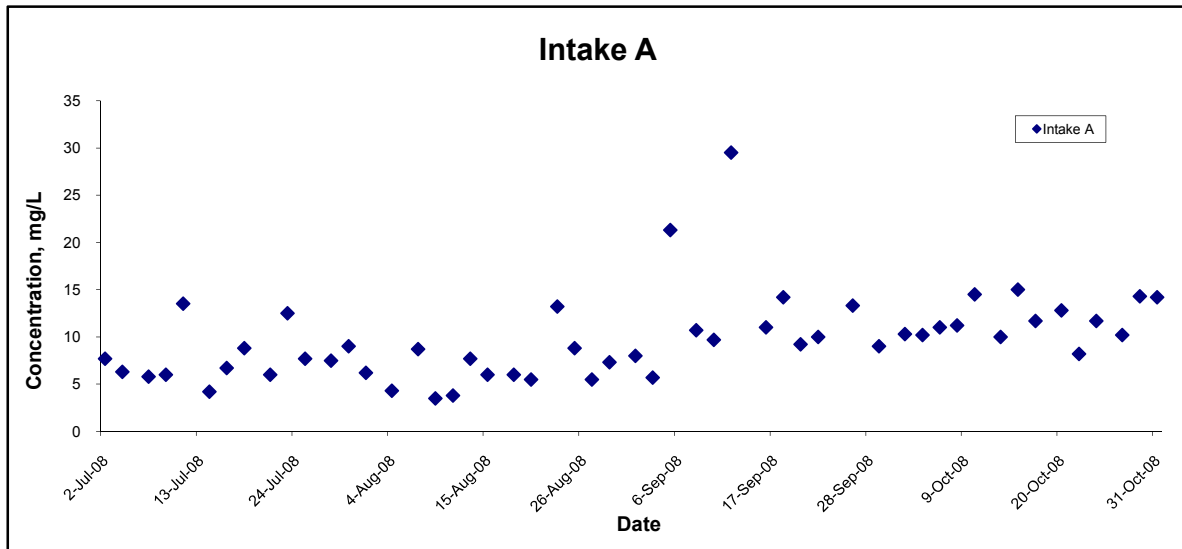



Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Suspended Solids (Depth-averaged) at Mid-Flood Tide

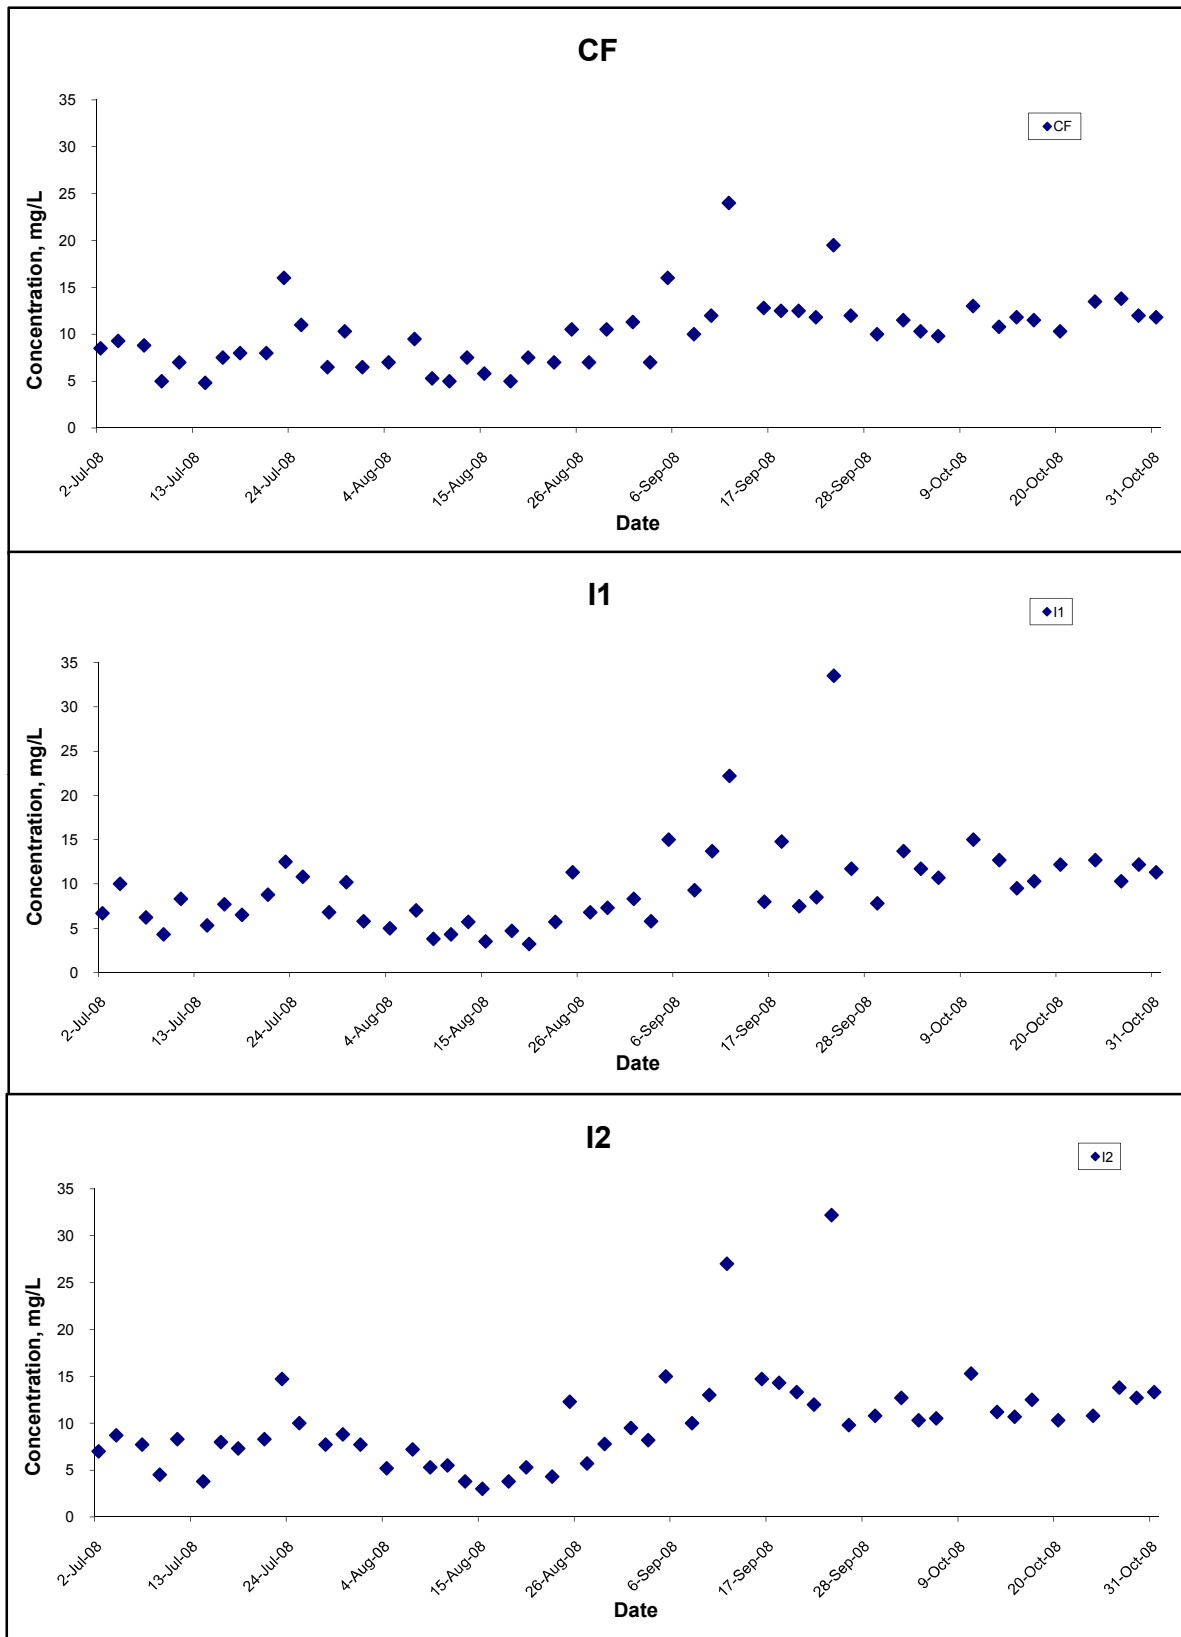

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale N.T.S	Project No. MA8001	CINOTECH
	Date Oct 08	Appendix H	

## Suspended Solids (Depth-averaged) at Mid-Flood Tide

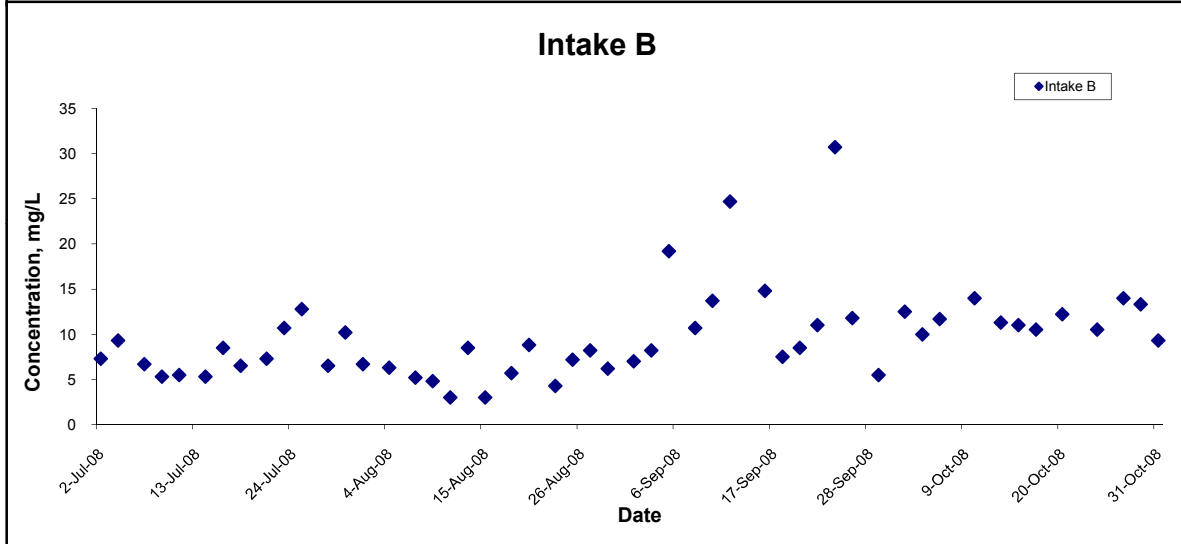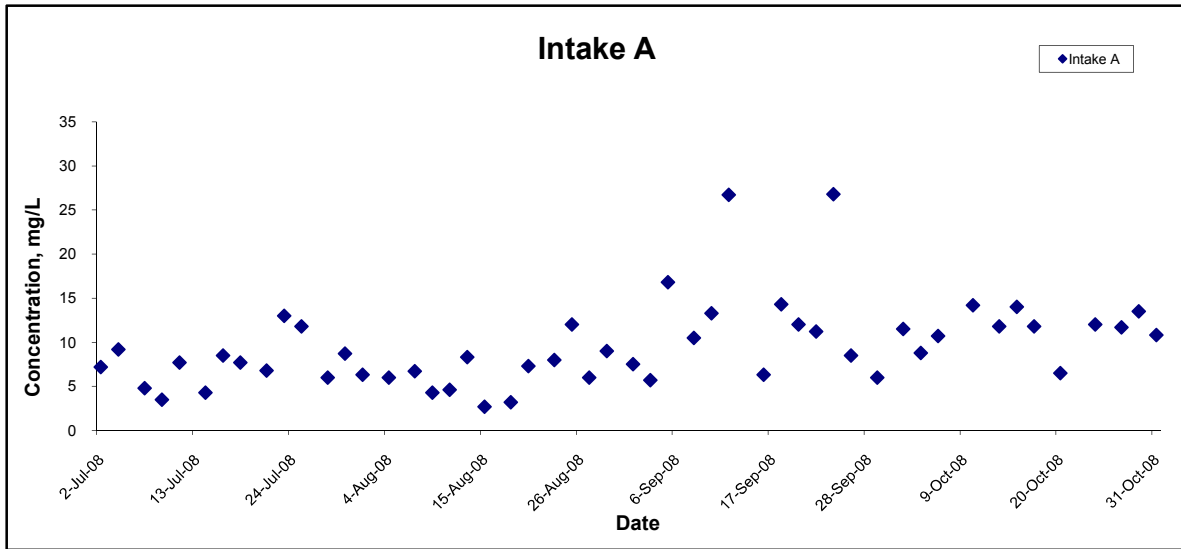

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel  Graphical Presentation of Water Quality Monitoring Results	Scale	N.T.S	Project No. MA8001	<b>CINOTECH</b>
	Date	Oct 08	Appendix H	

---

---

**APPENDIX I  
SUMMARY OF EXCEEDANCE**

---

---

**Contract No. DC/2007/10 – Design and Construction of Hong Kong West Drainage Tunnel**

**Exceedance Report**

**Eastern Portal**

**(A) Exceedance Report for Air Quality (1 hour TSP)  
(NIL in the reporting month)**

**(B) Exceedance Report for Air Quality (24 hours TSP)  
(NIL in the reporting month)**

**(C) Exceedance Report for Construction Noise  
(NIL in the reporting month)**

**Western Portal**

**(D) Exceedance Report for Air Quality (1 hour TSP)  
(NIL in the reporting month)**

**(E) Exceedance Report for Air Quality (24 hours TSP)  
(NIL in the reporting month)**

**(F) Exceedance Report for Construction Noise  
(NIL in the reporting month)**

**(G) Exceedance Report for Water Quality  
(NIL in the reporting month)**



---

---

**APPENDIX J**  
**WIND DATA**

---

---

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
1-Oct-2008	00:00	1.6	ENE
1-Oct-2008	01:00	1.5	ENE
1-Oct-2008	02:00	1.0	ENE
1-Oct-2008	03:00	1.3	ENE
1-Oct-2008	04:00	1.2	ENE
1-Oct-2008	05:00	1.0	NE
1-Oct-2008	06:00	1.2	NE
1-Oct-2008	07:00	1.2	ENE
1-Oct-2008	08:00	1.3	NE
1-Oct-2008	09:00	1.2	ENE
1-Oct-2008	10:00	1.5	NE
1-Oct-2008	11:00	1.5	ENE
1-Oct-2008	12:00	1.5	ENE
1-Oct-2008	13:00	1.3	ENE
1-Oct-2008	14:00	1.2	ENE
1-Oct-2008	15:00	1.3	N
1-Oct-2008	16:00	1.2	N
1-Oct-2008	17:00	0.9	NE
1-Oct-2008	18:00	0.7	ENE
1-Oct-2008	19:00	0.9	ENE
1-Oct-2008	20:00	1.3	ESE
1-Oct-2008	21:00	1.5	ESE
1-Oct-2008	22:00	1.3	SE
1-Oct-2008	23:00	1.5	SE
2-Oct-2008	00:00	1.3	SSE
2-Oct-2008	01:00	0.9	SSE
2-Oct-2008	02:00	1.0	SSE
2-Oct-2008	03:00	0.9	NE
2-Oct-2008	04:00	1.0	ENE
2-Oct-2008	05:00	0.1	ENE
2-Oct-2008	06:00	0	---
2-Oct-2008	07:00	0	---
2-Oct-2008	08:00	0	---
2-Oct-2008	09:00	0	---
2-Oct-2008	10:00	0.3	ENE
2-Oct-2008	11:00	0.1	ENE
2-Oct-2008	12:00	1.0	E
2-Oct-2008	13:00	1.2	NE
2-Oct-2008	14:00	1.3	NNE
2-Oct-2008	15:00	1.0	E
2-Oct-2008	16:00	0.3	E
2-Oct-2008	17:00	0.6	E
2-Oct-2008	18:00	0.3	E
2-Oct-2008	19:00	0	---
2-Oct-2008	20:00	0.3	E
2-Oct-2008	21:00	0.4	ENE
2-Oct-2008	22:00	0.4	ESE
2-Oct-2008	23:00	0.3	E
3-Oct-2008	00:00	0.4	ENE
3-Oct-2008	01:00	0.4	ENE
3-Oct-2008	02:00	0.3	ENE
3-Oct-2008	03:00	0.3	SSW
3-Oct-2008	04:00	0.4	ENE
3-Oct-2008	05:00	0.1	ENE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
3-Oct-2008	06:00	0	---
3-Oct-2008	07:00	0	---
3-Oct-2008	08:00	0	---
3-Oct-2008	09:00	0.1	SW
3-Oct-2008	10:00	0.3	SW
3-Oct-2008	11:00	0.7	S
3-Oct-2008	12:00	1.3	E
3-Oct-2008	13:00	1.6	ENE
3-Oct-2008	14:00	1.8	SE
3-Oct-2008	15:00	1.8	ESE
3-Oct-2008	16:00	1.6	NE
3-Oct-2008	17:00	1.3	E
3-Oct-2008	18:00	0.7	ENE
3-Oct-2008	19:00	0.9	N
3-Oct-2008	20:00	1.3	SE
3-Oct-2008	21:00	1.2	ESE
3-Oct-2008	22:00	1.2	NE
3-Oct-2008	23:00	1.8	N
4-Oct-2008	00:00	1.3	NE
4-Oct-2008	01:00	1.2	SW
4-Oct-2008	02:00	1.0	SE
4-Oct-2008	03:00	1.3	S
4-Oct-2008	04:00	1.5	SW
4-Oct-2008	05:00	1.6	S
4-Oct-2008	06:00	1.8	WSW
4-Oct-2008	07:00	1.5	NE
4-Oct-2008	08:00	1.3	NE
4-Oct-2008	09:00	1.6	SW
4-Oct-2008	10:00	2.4	SW
4-Oct-2008	11:00	2.7	SSE
4-Oct-2008	12:00	2.7	SSE
4-Oct-2008	13:00	2.7	SSE
4-Oct-2008	14:00	2.2	ESE
4-Oct-2008	15:00	2.1	ESE
4-Oct-2008	16:00	1.8	SE
4-Oct-2008	17:00	2.5	SSE
4-Oct-2008	18:00	2.2	SSE
4-Oct-2008	19:00	2.4	NNE
4-Oct-2008	20:00	2.5	NE
4-Oct-2008	21:00	1.8	NE
4-Oct-2008	22:00	1.9	NE
4-Oct-2008	23:00	2.1	NE
5-Oct-2008	00:00	2.2	ESE
5-Oct-2008	01:00	2.2	ESE
5-Oct-2008	02:00	3.0	ESE
5-Oct-2008	03:00	3.0	SE
5-Oct-2008	04:00	2.8	SSE
5-Oct-2008	05:00	3.0	SSE
5-Oct-2008	06:00	3.0	SSE
5-Oct-2008	07:00	3.0	SSE
5-Oct-2008	08:00	2.8	SW
5-Oct-2008	09:00	2.8	SSW
5-Oct-2008	10:00	2.7	SW
5-Oct-2008	11:00	3.3	WSW

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
5-Oct-2008	12:00	3.3	SW
5-Oct-2008	13:00	3.9	SW
5-Oct-2008	14:00	4.2	SW
5-Oct-2008	15:00	4.0	SW
5-Oct-2008	16:00	3.9	SW
5-Oct-2008	17:00	3.9	NE
5-Oct-2008	18:00	4.0	ENE
5-Oct-2008	19:00	4.0	ENE
5-Oct-2008	20:00	4.3	SE
5-Oct-2008	21:00	4.3	E
5-Oct-2008	22:00	4.6	SSE
5-Oct-2008	23:00	4.0	SSE
6-Oct-2008	00:00	1.2	SSE
6-Oct-2008	01:00	1.4	NNE
6-Oct-2008	02:00	0.8	NNE
6-Oct-2008	03:00	0.6	NNE
6-Oct-2008	04:00	0.6	NNE
6-Oct-2008	05:00	0.6	NE
6-Oct-2008	06:00	0.6	ENE
6-Oct-2008	07:00	1.1	ENE
6-Oct-2008	08:00	1.1	NE
6-Oct-2008	09:00	1.4	NNE
6-Oct-2008	10:00	1.6	NNE
6-Oct-2008	11:00	1.9	ENE
6-Oct-2008	12:00	1.6	ENE
6-Oct-2008	13:00	2.2	ENE
6-Oct-2008	14:00	2.5	NE
6-Oct-2008	15:00	2.7	NE
6-Oct-2008	16:00	1.8	NNE
6-Oct-2008	17:00	1.4	ENE
6-Oct-2008	18:00	1.4	ENE
6-Oct-2008	19:00	1.2	ENE
6-Oct-2008	20:00	1.6	ENE
6-Oct-2008	21:00	1.5	ENE
6-Oct-2008	22:00	1.7	ENE
6-Oct-2008	23:00	1.6	NNE
7-Oct-2008	00:00	1.1	N
7-Oct-2008	01:00	0.9	N
7-Oct-2008	02:00	0.8	NNE
7-Oct-2008	03:00	0.9	N
7-Oct-2008	04:00	0.9	ENE
7-Oct-2008	05:00	1.4	ENE
7-Oct-2008	06:00	1.5	ESE
7-Oct-2008	07:00	1.2	ESE
7-Oct-2008	08:00	1.5	ENE
7-Oct-2008	09:00	1.4	ENE
7-Oct-2008	10:00	1.5	ENE
7-Oct-2008	11:00	1.7	NNE
7-Oct-2008	12:00	3.2	ENE
7-Oct-2008	13:00	2.4	ENE
7-Oct-2008	14:00	2.0	ENE
7-Oct-2008	15:00	1.6	ENE
7-Oct-2008	16:00	1.7	ENE
7-Oct-2008	17:00	1.8	E

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
7-Oct-2008	18:00	1.2	E
7-Oct-2008	19:00	1.0	E
7-Oct-2008	20:00	0.6	E
7-Oct-2008	21:00	0.6	E
7-Oct-2008	22:00	0.8	E
7-Oct-2008	23:00	0.5	E
8-Oct-2008	00:00	0	---
8-Oct-2008	01:00	0	---
8-Oct-2008	02:00	0	---
8-Oct-2008	03:00	0	---
8-Oct-2008	04:00	0	---
8-Oct-2008	05:00	0.2	NNE
8-Oct-2008	06:00	0	---
8-Oct-2008	07:00	0.2	ENE
8-Oct-2008	08:00	0.5	ENE
8-Oct-2008	09:00	1.1	ENE
8-Oct-2008	10:00	1.9	ENE
8-Oct-2008	11:00	1.5	ENE
8-Oct-2008	12:00	1.7	ENE
8-Oct-2008	13:00	1.5	ENE
8-Oct-2008	14:00	1.5	ENE
8-Oct-2008	15:00	1.5	ENE
8-Oct-2008	16:00	1.4	ENE
8-Oct-2008	17:00	2.0	ESE
8-Oct-2008	18:00	0.8	ESE
8-Oct-2008	19:00	1.4	ESE
8-Oct-2008	20:00	1.1	ESE
8-Oct-2008	21:00	1.3	ESE
8-Oct-2008	22:00	1.5	SSW
8-Oct-2008	23:00	1.6	W
9-Oct-2008	00:00	1.9	SW
9-Oct-2008	01:00	1.8	SW
9-Oct-2008	02:00	1.2	W
9-Oct-2008	03:00	1.2	E
9-Oct-2008	04:00	0.9	S
9-Oct-2008	05:00	0.6	E
9-Oct-2008	06:00	0.8	SW
9-Oct-2008	07:00	0.5	WSW
9-Oct-2008	08:00	1.2	N
9-Oct-2008	09:00	2.3	N
9-Oct-2008	10:00	2.9	NE
9-Oct-2008	11:00	3.0	ENE
9-Oct-2008	12:00	2.7	ENE
9-Oct-2008	13:00	2.0	WNW
9-Oct-2008	14:00	2.2	NW
9-Oct-2008	15:00	2.1	E
9-Oct-2008	16:00	1.7	E
9-Oct-2008	17:00	1.5	SE
9-Oct-2008	18:00	1.1	N
9-Oct-2008	19:00	0.5	N
9-Oct-2008	20:00	0.2	N
9-Oct-2008	21:00	0.9	NNE
9-Oct-2008	22:00	1.1	NNE
9-Oct-2008	23:00	0.9	N

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
10-Oct-2008	00:00	1.0	N
10-Oct-2008	01:00	1.5	N
10-Oct-2008	02:00	2.0	NNE
10-Oct-2008	03:00	2.4	NNE
10-Oct-2008	04:00	2.4	N
10-Oct-2008	05:00	2.3	NNE
10-Oct-2008	06:00	1.7	NNE
10-Oct-2008	07:00	2.0	NE
10-Oct-2008	08:00	2.4	NE
10-Oct-2008	09:00	2.6	NNE
10-Oct-2008	10:00	3.6	ENE
10-Oct-2008	11:00	2.9	ENE
10-Oct-2008	12:00	3.2	ENE
10-Oct-2008	13:00	3.3	ENE
10-Oct-2008	14:00	2.0	ENE
10-Oct-2008	15:00	1.3	NNE
10-Oct-2008	16:00	1.6	NNE
10-Oct-2008	17:00	1.4	NNE
10-Oct-2008	18:00	1.2	NNE
10-Oct-2008	19:00	1.4	NE
10-Oct-2008	20:00	1.3	NE
10-Oct-2008	21:00	0.9	NNE
10-Oct-2008	22:00	0.3	NE
10-Oct-2008	23:00	1.0	NE
11-Oct-2008	00:00	1.9	ENE
11-Oct-2008	01:00	1.4	ENE
11-Oct-2008	02:00	1.4	NE
11-Oct-2008	03:00	0.2	NE
11-Oct-2008	04:00	1.0	NE
11-Oct-2008	05:00	1.9	NE
11-Oct-2008	06:00	2.4	NE
11-Oct-2008	07:00	1.7	NE
11-Oct-2008	08:00	1.7	NE
11-Oct-2008	09:00	2.8	ENE
11-Oct-2008	10:00	2.5	NE
11-Oct-2008	11:00	2.3	NE
11-Oct-2008	12:00	2.7	NE
11-Oct-2008	13:00	2.8	NE
11-Oct-2008	14:00	3.3	NE
11-Oct-2008	15:00	3.3	NNE
11-Oct-2008	16:00	2.4	NE
11-Oct-2008	17:00	3.2	NE
11-Oct-2008	18:00	2.9	ENE
11-Oct-2008	19:00	1.3	ENE
11-Oct-2008	20:00	1.9	N
11-Oct-2008	21:00	1.9	NNE
11-Oct-2008	22:00	0.9	NNE
11-Oct-2008	23:00	1.2	ENE
12-Oct-2008	00:00	1.3	NE
12-Oct-2008	01:00	1.4	NNE
12-Oct-2008	02:00	0.7	NNE
12-Oct-2008	03:00	1.3	NE
12-Oct-2008	04:00	1.3	NE
12-Oct-2008	05:00	1.6	NE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
12-Oct-2008	06:00	0.8	ENE
12-Oct-2008	07:00	0.9	ENE
12-Oct-2008	08:00	1.6	NE
12-Oct-2008	09:00	1.9	ENE
12-Oct-2008	10:00	2.5	ENE
12-Oct-2008	11:00	2.4	ENE
12-Oct-2008	12:00	3.6	NE
12-Oct-2008	13:00	3.9	NE
12-Oct-2008	14:00	2.9	NNE
12-Oct-2008	15:00	2.2	NNE
12-Oct-2008	16:00	2.4	NNE
12-Oct-2008	17:00	2.6	WNW
12-Oct-2008	18:00	2.1	WNW
12-Oct-2008	19:00	1.8	WNW
12-Oct-2008	20:00	1.3	WNW
12-Oct-2008	21:00	1.3	NNE
12-Oct-2008	22:00	1.5	NNE
12-Oct-2008	23:00	2.1	NE
13-Oct-2008	00:00	2.4	NW
13-Oct-2008	01:00	2.4	NW
13-Oct-2008	02:00	1.9	NNE
13-Oct-2008	03:00	1.9	SE
13-Oct-2008	04:00	1.0	SE
13-Oct-2008	05:00	1.5	SE
13-Oct-2008	06:00	1.7	NE
13-Oct-2008	07:00	1.5	NNE
13-Oct-2008	08:00	1.5	NNE
13-Oct-2008	09:00	1.8	N
13-Oct-2008	10:00	2.4	NE
13-Oct-2008	11:00	3.1	NE
13-Oct-2008	12:00	4.0	NNE
13-Oct-2008	13:00	3.7	NE
13-Oct-2008	14:00	3.4	NE
13-Oct-2008	15:00	3.4	NE
13-Oct-2008	16:00	2.4	NNE
13-Oct-2008	17:00	2.2	ENE
13-Oct-2008	18:00	2.3	NE
13-Oct-2008	19:00	2.4	NE
13-Oct-2008	20:00	2.4	NNE
13-Oct-2008	21:00	2.7	NE
13-Oct-2008	22:00	1.8	ENE
13-Oct-2008	23:00	2.0	ENE
14-Oct-2008	00:00	2.1	SSE
14-Oct-2008	01:00	1.7	SSE
14-Oct-2008	02:00	1.9	ESE
14-Oct-2008	03:00	1.2	SSE
14-Oct-2008	04:00	1.5	ESE
14-Oct-2008	05:00	1.5	ESE
14-Oct-2008	06:00	1.1	NE
14-Oct-2008	07:00	2.0	NE
14-Oct-2008	08:00	2.0	NE
14-Oct-2008	09:00	2.9	ESE
14-Oct-2008	10:00	2.8	ESE
14-Oct-2008	11:00	2.5	NE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
14-Oct-2008	12:00	3.0	NE
14-Oct-2008	13:00	2.9	NE
14-Oct-2008	14:00	2.1	NE
14-Oct-2008	15:00	2.9	E
14-Oct-2008	16:00	2.5	NNE
14-Oct-2008	17:00	1.8	NNE
14-Oct-2008	18:00	1.5	NNE
14-Oct-2008	19:00	2.1	NNE
14-Oct-2008	20:00	1.8	ENE
14-Oct-2008	21:00	2.7	NE
14-Oct-2008	22:00	2.2	NE
14-Oct-2008	23:00	1.7	NE
15-Oct-2008	00:00	2.4	NE
15-Oct-2008	01:00	1.7	NE
15-Oct-2008	02:00	2.1	NNE
15-Oct-2008	03:00	2.6	NE
15-Oct-2008	04:00	1.8	NE
15-Oct-2008	05:00	1.5	N
15-Oct-2008	06:00	2.1	NE
15-Oct-2008	07:00	2.2	NE
15-Oct-2008	08:00	2.3	NE
15-Oct-2008	09:00	2.8	NE
15-Oct-2008	10:00	3.5	ENE
15-Oct-2008	11:00	3.1	ENE
15-Oct-2008	12:00	3.2	NE
15-Oct-2008	13:00	2.8	ENE
15-Oct-2008	14:00	3.1	ENE
15-Oct-2008	15:00	2.9	ENE
15-Oct-2008	16:00	3.0	E
15-Oct-2008	17:00	2.8	NNE
15-Oct-2008	18:00	2.3	N
15-Oct-2008	19:00	2.1	NNW
15-Oct-2008	20:00	1.8	W
15-Oct-2008	21:00	1.5	W
15-Oct-2008	22:00	1.8	NE
15-Oct-2008	23:00	1.7	SSW
16-Oct-2008	00:00	1.8	W
16-Oct-2008	01:00	1.8	SW
16-Oct-2008	02:00	1.2	SSE
16-Oct-2008	03:00	1.3	SSE
16-Oct-2008	04:00	1.9	SE
16-Oct-2008	05:00	2.2	SE
16-Oct-2008	06:00	1.9	ENE
16-Oct-2008	07:00	2.3	ENE
16-Oct-2008	08:00	2.1	ENE
16-Oct-2008	09:00	2.5	ENE
16-Oct-2008	10:00	1.8	ENE
16-Oct-2008	11:00	1.9	ENE
16-Oct-2008	12:00	2.5	ENE
16-Oct-2008	13:00	3.2	ENE
16-Oct-2008	14:00	2.9	ENE
16-Oct-2008	15:00	2.6	ENE
16-Oct-2008	16:00	2.6	ENE
16-Oct-2008	17:00	2.6	NE



## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
16-Oct-2008	18:00	1.7	E
16-Oct-2008	19:00	1.8	ENE
16-Oct-2008	20:00	1.2	ENE
16-Oct-2008	21:00	1.2	NE
16-Oct-2008	22:00	0.8	ENE
16-Oct-2008	23:00	1.3	NE
17-Oct-2008	00:00	1.5	ENE
17-Oct-2008	01:00	1.6	ENE
17-Oct-2008	02:00	1.5	NE
17-Oct-2008	03:00	2.0	NE
17-Oct-2008	04:00	1.4	NE
17-Oct-2008	05:00	1.2	NE
17-Oct-2008	06:00	1.5	ENE
17-Oct-2008	07:00	1.8	ENE
17-Oct-2008	08:00	2.1	ENE
17-Oct-2008	09:00	1.7	NE
17-Oct-2008	10:00	2.1	NE
17-Oct-2008	11:00	2.7	ENE
17-Oct-2008	12:00	2.6	ENE
17-Oct-2008	13:00	2.1	NE
17-Oct-2008	14:00	2.4	NE
17-Oct-2008	15:00	2.8	NE
17-Oct-2008	16:00	2.3	ENE
17-Oct-2008	17:00	1.6	ENE
17-Oct-2008	18:00	1.0	NE
17-Oct-2008	19:00	0.8	NE
17-Oct-2008	20:00	0.8	NNE
17-Oct-2008	21:00	0.6	ENE
17-Oct-2008	22:00	1.1	ENE
17-Oct-2008	23:00	0.5	ENE
18-Oct-2008	00:00	0.2	NE
18-Oct-2008	01:00	0.5	NE
18-Oct-2008	02:00	0.0	ENE
18-Oct-2008	03:00	0.2	ENE
18-Oct-2008	04:00	0.2	NNE
18-Oct-2008	05:00	0.3	N
18-Oct-2008	06:00	0.0	N
18-Oct-2008	07:00	0.0	W
18-Oct-2008	08:00	0.5	N
18-Oct-2008	09:00	1.9	N
18-Oct-2008	10:00	2.3	N
18-Oct-2008	11:00	2.4	N
18-Oct-2008	12:00	2.3	N
18-Oct-2008	13:00	1.8	NE
18-Oct-2008	14:00	1.3	ENE
18-Oct-2008	15:00	1.2	ENE
18-Oct-2008	16:00	1.2	NE
18-Oct-2008	17:00	1.0	ENE
18-Oct-2008	18:00	1.3	E
18-Oct-2008	19:00	0.5	ENE
18-Oct-2008	20:00	1.2	ENE
18-Oct-2008	21:00	1.2	ENE
18-Oct-2008	22:00	0.6	ENE
18-Oct-2008	23:00	1.1	ENE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
19-Oct-2008	00:00	1.2	ENE
19-Oct-2008	01:00	0.9	SSE
19-Oct-2008	02:00	1.5	SSE
19-Oct-2008	03:00	1.2	SSE
19-Oct-2008	04:00	0.9	SE
19-Oct-2008	05:00	1.2	SE
19-Oct-2008	06:00	1.2	SSE
19-Oct-2008	07:00	0.9	SSE
19-Oct-2008	08:00	1.1	E
19-Oct-2008	09:00	0.8	E
19-Oct-2008	10:00	2.6	E
19-Oct-2008	11:00	3.0	E
19-Oct-2008	12:00	2.6	E
19-Oct-2008	13:00	1.7	E
19-Oct-2008	14:00	2.1	ESE
19-Oct-2008	15:00	2.3	SE
19-Oct-2008	16:00	2.7	SSE
19-Oct-2008	17:00	2.6	SSE
19-Oct-2008	18:00	2.4	SE
19-Oct-2008	19:00	1.2	SE
19-Oct-2008	20:00	0.5	SE
19-Oct-2008	21:00	0.2	SW
19-Oct-2008	22:00	0.2	ESE
19-Oct-2008	23:00	0.5	E
20-Oct-2008	00:00	0.3	ESE
20-Oct-2008	01:00	0.2	ESE
20-Oct-2008	02:00	0.6	SSE
20-Oct-2008	03:00	0.3	SSE
20-Oct-2008	04:00	0.3	ENE
20-Oct-2008	05:00	0.0	NE
20-Oct-2008	06:00	0.0	ENE
20-Oct-2008	07:00	0.2	SE
20-Oct-2008	08:00	1.6	SE
20-Oct-2008	09:00	2.2	SE
20-Oct-2008	10:00	3.3	SSE
20-Oct-2008	11:00	3.1	SSE
20-Oct-2008	12:00	3.3	SE
20-Oct-2008	13:00	3.1	S
20-Oct-2008	14:00	2.3	SSE
20-Oct-2008	15:00	2.2	ESE
20-Oct-2008	16:00	1.8	S
20-Oct-2008	17:00	1.3	S
20-Oct-2008	18:00	0.8	S
20-Oct-2008	19:00	0.5	SE
20-Oct-2008	20:00	0.0	SE
20-Oct-2008	21:00	0.0	ESE
20-Oct-2008	22:00	0.0	S
20-Oct-2008	23:00	0.0	ENE
21-Oct-2008	00:00	0.9	ENE
21-Oct-2008	01:00	1.0	NE
21-Oct-2008	02:00	1.1	NE
21-Oct-2008	03:00	1.2	NE
21-Oct-2008	04:00	1.0	NE
21-Oct-2008	05:00	0.5	NE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
21-Oct-2008	06:00	0.4	NNE
21-Oct-2008	07:00	0.2	NE
21-Oct-2008	08:00	0.0	NE
21-Oct-2008	09:00	1.8	NNE
21-Oct-2008	10:00	1.8	SE
21-Oct-2008	11:00	1.8	SE
21-Oct-2008	12:00	1.5	SE
21-Oct-2008	13:00	1.0	E
21-Oct-2008	14:00	1.0	ESE
21-Oct-2008	15:00	1.5	SSE
21-Oct-2008	16:00	1.8	SSE
21-Oct-2008	17:00	1.8	SE
21-Oct-2008	18:00	0.8	SE
21-Oct-2008	19:00	0.6	SE
21-Oct-2008	20:00	0.9	SSE
21-Oct-2008	21:00	0.9	SE
21-Oct-2008	22:00	0.9	SSE
21-Oct-2008	23:00	1.1	SSE
22-Oct-2008	00:00	1.2	SSE
22-Oct-2008	01:00	1.1	SE
22-Oct-2008	02:00	1.2	ESE
22-Oct-2008	03:00	0.6	ESE
22-Oct-2008	04:00	1.2	ESE
22-Oct-2008	05:00	1.1	SSE
22-Oct-2008	06:00	0.8	SE
22-Oct-2008	07:00	1.0	SE
22-Oct-2008	08:00	1.9	SE
22-Oct-2008	09:00	1.7	SE
22-Oct-2008	10:00	1.8	E
22-Oct-2008	11:00	1.6	SSE
22-Oct-2008	12:00	2.2	SSE
22-Oct-2008	13:00	2.1	SSE
22-Oct-2008	14:00	2.2	SW
22-Oct-2008	15:00	2.2	SW
22-Oct-2008	16:00	3.0	SW
22-Oct-2008	17:00	1.9	SSW
22-Oct-2008	18:00	1.4	SW
22-Oct-2008	19:00	2.3	SSW
22-Oct-2008	20:00	2.2	SW
22-Oct-2008	21:00	2.5	W
22-Oct-2008	22:00	2.5	W
22-Oct-2008	23:00	1.9	WNW
23-Oct-2008	00:00	2.3	WNW
23-Oct-2008	01:00	2.3	WNW
23-Oct-2008	02:00	2.2	WNW
23-Oct-2008	03:00	1.8	W
23-Oct-2008	04:00	2.3	WNW
23-Oct-2008	05:00	2.4	NW
23-Oct-2008	06:00	1.9	WNW
23-Oct-2008	07:00	1.8	WNW
23-Oct-2008	08:00	2.3	W
23-Oct-2008	09:00	2.1	W
23-Oct-2008	10:00	2.9	WNW
23-Oct-2008	11:00	3.3	NE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
23-Oct-2008	12:00	3.5	NE
23-Oct-2008	13:00	3.5	NNE
23-Oct-2008	14:00	3.8	NE
23-Oct-2008	15:00	2.9	NE
23-Oct-2008	16:00	2.6	NNE
23-Oct-2008	17:00	3.1	NNE
23-Oct-2008	18:00	2.4	NE
23-Oct-2008	19:00	2.6	NNE
23-Oct-2008	20:00	3.2	NNE
23-Oct-2008	21:00	2.9	NE
23-Oct-2008	22:00	3.0	NE
23-Oct-2008	23:00	2.6	NNE
24-Oct-2008	00:00	3.1	NNE
24-Oct-2008	01:00	2.7	ENE
24-Oct-2008	02:00	2.8	NNE
24-Oct-2008	03:00	2.3	E
24-Oct-2008	04:00	1.6	ESE
24-Oct-2008	05:00	2.3	ESE
24-Oct-2008	06:00	2.1	N
24-Oct-2008	07:00	2.2	N
24-Oct-2008	08:00	3.2	N
24-Oct-2008	09:00	3.5	N
24-Oct-2008	10:00	3.9	NNE
24-Oct-2008	11:00	4.3	NNE
24-Oct-2008	12:00	4.2	NE
24-Oct-2008	13:00	4.6	NNE
24-Oct-2008	14:00	4.2	NNE
24-Oct-2008	15:00	4.1	NNE
24-Oct-2008	16:00	4.6	NNE
24-Oct-2008	17:00	4.9	NNE
24-Oct-2008	18:00	2.4	NNE
24-Oct-2008	19:00	2.4	NNE
24-Oct-2008	20:00	1.9	NNE
24-Oct-2008	21:00	1.4	NNE
24-Oct-2008	22:00	2.4	NNE
24-Oct-2008	23:00	2.5	ENE
25-Oct-2008	00:00	2.1	NE
25-Oct-2008	01:00	2.4	ENE
25-Oct-2008	02:00	2.4	ENE
25-Oct-2008	03:00	2.3	NE
25-Oct-2008	04:00	1.8	NE
25-Oct-2008	05:00	2.0	NE
25-Oct-2008	06:00	2.0	ENE
25-Oct-2008	07:00	1.4	E
25-Oct-2008	08:00	1.9	E
25-Oct-2008	09:00	3.3	E
25-Oct-2008	10:00	3.9	SE
25-Oct-2008	11:00	3.9	SSE
25-Oct-2008	12:00	2.5	SE
25-Oct-2008	13:00	3.1	SE
25-Oct-2008	14:00	3.1	SE
25-Oct-2008	15:00	3.1	SE
25-Oct-2008	16:00	2.5	SE
25-Oct-2008	17:00	1.8	SE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
25-Oct-2008	18:00	1.5	NE
25-Oct-2008	19:00	1.2	E
25-Oct-2008	20:00	1.5	ENE
25-Oct-2008	21:00	1.1	ENE
25-Oct-2008	22:00	1.3	ENE
25-Oct-2008	23:00	2.0	ENE
26-Oct-2008	00:00	1.8	NE
26-Oct-2008	01:00	1.6	ENE
26-Oct-2008	02:00	1.2	ENE
26-Oct-2008	03:00	0.8	N
26-Oct-2008	04:00	1.6	N
26-Oct-2008	05:00	1.0	NNE
26-Oct-2008	06:00	0.4	N
26-Oct-2008	07:00	0.2	NNE
26-Oct-2008	08:00	1.2	N
26-Oct-2008	09:00	2.5	NNE
26-Oct-2008	10:00	2.7	NNE
26-Oct-2008	11:00	1.6	NNE
26-Oct-2008	12:00	2.4	NE
26-Oct-2008	13:00	2.7	NNE
26-Oct-2008	14:00	3.1	NNE
26-Oct-2008	15:00	3.1	NNE
26-Oct-2008	16:00	2.1	E
26-Oct-2008	17:00	1.5	E
26-Oct-2008	18:00	0.5	E
26-Oct-2008	19:00	0.3	NNE
26-Oct-2008	20:00	0.6	NNE
26-Oct-2008	21:00	0.9	NNE
26-Oct-2008	22:00	1.1	NNE
26-Oct-2008	23:00	0.9	ENE
27-Oct-2008	00:00	0.6	ENE
27-Oct-2008	01:00	0.8	NE
27-Oct-2008	02:00	0.6	NE
27-Oct-2008	03:00	1.8	NNE
27-Oct-2008	04:00	1.5	NE
27-Oct-2008	05:00	1.6	N
27-Oct-2008	06:00	1.6	NE
27-Oct-2008	07:00	1.6	NNE
27-Oct-2008	08:00	2.2	NNE
27-Oct-2008	09:00	2.7	NE
27-Oct-2008	10:00	2.4	NE
27-Oct-2008	11:00	3.6	ENE
27-Oct-2008	12:00	3.3	E
27-Oct-2008	13:00	3.0	ENE
27-Oct-2008	14:00	3.3	NE
27-Oct-2008	15:00	2.7	NE
27-Oct-2008	16:00	3.0	NE
27-Oct-2008	17:00	2.4	E
27-Oct-2008	18:00	2.0	ENE
27-Oct-2008	19:00	2.0	ENE
27-Oct-2008	20:00	2.5	NE
27-Oct-2008	21:00	2.5	E
27-Oct-2008	22:00	1.7	E
27-Oct-2008	23:00	1.5	ENE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
28-Oct-2008	00:00	1.3	ENE
28-Oct-2008	01:00	1.5	ENE
28-Oct-2008	02:00	1.5	ENE
28-Oct-2008	03:00	1.3	ENE
28-Oct-2008	04:00	1.1	NE
28-Oct-2008	05:00	1.1	NE
28-Oct-2008	06:00	1.1	ENE
28-Oct-2008	07:00	1.1	ENE
28-Oct-2008	08:00	1.3	NE
28-Oct-2008	09:00	2.4	NE
28-Oct-2008	10:00	3.6	NNE
28-Oct-2008	11:00	3.9	NNE
28-Oct-2008	12:00	3.1	NE
28-Oct-2008	13:00	3.3	ENE
28-Oct-2008	14:00	2.9	N
28-Oct-2008	15:00	2.8	N
28-Oct-2008	16:00	2.8	E
28-Oct-2008	17:00	2.4	ENE
28-Oct-2008	18:00	1.8	ENE
28-Oct-2008	19:00	1.6	ENE
28-Oct-2008	20:00	1.2	ENE
28-Oct-2008	21:00	1.5	E
28-Oct-2008	22:00	1.2	NE
28-Oct-2008	23:00	1.2	NE
29-Oct-2008	00:00	1.2	NE
29-Oct-2008	01:00	1.2	NNE
29-Oct-2008	02:00	1.2	E
29-Oct-2008	03:00	1.0	E
29-Oct-2008	04:00	1.6	E
29-Oct-2008	05:00	1.4	NE
29-Oct-2008	06:00	1.2	NE
29-Oct-2008	07:00	1.4	NE
29-Oct-2008	08:00	1.4	NE
29-Oct-2008	09:00	2.2	NE
29-Oct-2008	10:00	2.8	NE
29-Oct-2008	11:00	2.4	NNE
29-Oct-2008	12:00	2.4	NNE
29-Oct-2008	13:00	2.0	NNE
29-Oct-2008	14:00	1.8	NNE
29-Oct-2008	15:00	2.3	NE
29-Oct-2008	16:00	1.6	ENE
29-Oct-2008	17:00	1.6	ENE
29-Oct-2008	18:00	0.9	NE
29-Oct-2008	19:00	0.3	NE
29-Oct-2008	20:00	0.3	NE
29-Oct-2008	21:00	0.2	ENE
29-Oct-2008	22:00	0.5	ENE
29-Oct-2008	23:00	0.3	NE
30-Oct-2008	00:00	0.3	NE
30-Oct-2008	01:00	0.5	ESE
30-Oct-2008	02:00	0.5	ESE
30-Oct-2008	03:00	0.5	NNE
30-Oct-2008	04:00	0.5	NNE
30-Oct-2008	05:00	0.3	NNE

## Appendix J - Wind Data (Eastern Portal)

Date	Time	Wind Speed m/s	Direction
30-Oct-2008	06:00	0.5	NNE
30-Oct-2008	07:00	1.4	NNE
30-Oct-2008	08:00	1.5	NNE
30-Oct-2008	09:00	1.7	NNE
30-Oct-2008	10:00	1.6	NNE
30-Oct-2008	11:00	1.7	NNE
30-Oct-2008	12:00	1.7	NNE
30-Oct-2008	13:00	1.2	NNE
30-Oct-2008	14:00	1.1	WNW
30-Oct-2008	15:00	1.7	N
30-Oct-2008	16:00	1.1	N
30-Oct-2008	17:00	1.4	N
30-Oct-2008	18:00	0.8	NNE
30-Oct-2008	19:00	1.0	NNE
30-Oct-2008	20:00	0.6	NNE
30-Oct-2008	21:00	0.4	NNE
30-Oct-2008	22:00	0.2	NNE
30-Oct-2008	23:00	0.6	N
31-Oct-2008	00:00	1.5	NNE
31-Oct-2008	01:00	1.3	NNE
31-Oct-2008	02:00	1.5	NNE
31-Oct-2008	03:00	1.3	NNE
31-Oct-2008	04:00	1.6	NE
31-Oct-2008	05:00	0.7	NE
31-Oct-2008	06:00	0.6	NE
31-Oct-2008	07:00	0.7	NNE
31-Oct-2008	08:00	0.8	ENE
31-Oct-2008	09:00	0.8	ENE
31-Oct-2008	10:00	0.8	NE
31-Oct-2008	11:00	1.8	ENE
31-Oct-2008	12:00	2.2	NE
31-Oct-2008	13:00	2.4	NE
31-Oct-2008	14:00	2.6	NE
31-Oct-2008	15:00	3.1	NE
31-Oct-2008	16:00	2.6	NE
31-Oct-2008	17:00	2.5	NE
31-Oct-2008	18:00	1.9	ENE
31-Oct-2008	19:00	1.8	NE
31-Oct-2008	20:00	1.2	ENE
31-Oct-2008	21:00	0.9	ENE
31-Oct-2008	22:00	1.1	ENE
31-Oct-2008	23:00	1.1	ENE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
1-Oct-2008	00:00	2.7	SW
1-Oct-2008	01:00	2.6	W
1-Oct-2008	02:00	2.0	WSW
1-Oct-2008	03:00	1.7	WSW
1-Oct-2008	04:00	1.7	WSW
1-Oct-2008	05:00	2.0	WNW
1-Oct-2008	06:00	1.7	WNW
1-Oct-2008	07:00	2.1	NE
1-Oct-2008	08:00	1.2	NE
1-Oct-2008	09:00	1.7	NE
1-Oct-2008	10:00	1.7	WNW
1-Oct-2008	11:00	2.1	NW
1-Oct-2008	12:00	2.6	E
1-Oct-2008	13:00	2.4	E
1-Oct-2008	14:00	2.7	ESE
1-Oct-2008	15:00	2.4	ESE
1-Oct-2008	16:00	2.7	ESE
1-Oct-2008	17:00	2.2	ESE
1-Oct-2008	18:00	1.9	SE
1-Oct-2008	19:00	1.1	SE
1-Oct-2008	20:00	1.0	W
1-Oct-2008	21:00	1.2	W
1-Oct-2008	22:00	1.6	W
1-Oct-2008	23:00	1.4	SW
2-Oct-2008	00:00	1.6	SW
2-Oct-2008	01:00	2.3	WSW
2-Oct-2008	02:00	2.5	W
2-Oct-2008	03:00	2.3	WSW
2-Oct-2008	04:00	2.1	NE
2-Oct-2008	05:00	1.9	NE
2-Oct-2008	06:00	2.1	NNE
2-Oct-2008	07:00	1.7	ENE
2-Oct-2008	08:00	1.8	ENE
2-Oct-2008	09:00	1.7	N
2-Oct-2008	10:00	1.7	W
2-Oct-2008	11:00	1.4	WNW
2-Oct-2008	12:00	1.5	WNW
2-Oct-2008	13:00	1.2	WNW
2-Oct-2008	14:00	1.3	W
2-Oct-2008	15:00	1.4	W
2-Oct-2008	16:00	1.4	WNW
2-Oct-2008	17:00	1.2	SW
2-Oct-2008	18:00	1.1	SSW
2-Oct-2008	19:00	0.6	SSE
2-Oct-2008	20:00	0.7	NNE
2-Oct-2008	21:00	0.8	NNE
2-Oct-2008	22:00	1.1	NNE
2-Oct-2008	23:00	1.0	N
3-Oct-2008	00:00	1.2	NE
3-Oct-2008	01:00	1.1	N
3-Oct-2008	02:00	1.3	N
3-Oct-2008	03:00	1.9	ENE
3-Oct-2008	04:00	2.2	ENE
3-Oct-2008	05:00	2.0	ENE



## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
3-Oct-2008	06:00	2.4	ENE
3-Oct-2008	07:00	2.6	E
3-Oct-2008	08:00	2.0	ENE
3-Oct-2008	09:00	2.0	SE
3-Oct-2008	10:00	2.3	N
3-Oct-2008	11:00	2.3	N
3-Oct-2008	12:00	2.4	NNE
3-Oct-2008	13:00	2	ENE
3-Oct-2008	14:00	2	ENE
3-Oct-2008	15:00	2	NE
3-Oct-2008	16:00	2	NE
3-Oct-2008	17:00	1.4	NE
3-Oct-2008	18:00	1.9	NNE
3-Oct-2008	19:00	1.9	NNE
3-Oct-2008	20:00	1.8	NNE
3-Oct-2008	21:00	1.3	NE
3-Oct-2008	22:00	1.5	NE
3-Oct-2008	23:00	1.1	ENE
4-Oct-2008	00:00	1.7	ENE
4-Oct-2008	01:00	2	NE
4-Oct-2008	02:00	2	E
4-Oct-2008	03:00	2	E
4-Oct-2008	04:00	1.5	ESE
4-Oct-2008	05:00	1.3	ESE
4-Oct-2008	06:00	1.5	ESE
4-Oct-2008	07:00	1.4	NNE
4-Oct-2008	08:00	1.7	NNE
4-Oct-2008	09:00	1.8	NNE
4-Oct-2008	10:00	2.0	SSE
4-Oct-2008	11:00	2.3	NE
4-Oct-2008	12:00	2.7	ENE
4-Oct-2008	13:00	2.5	SSE
4-Oct-2008	14:00	2.9	N
4-Oct-2008	15:00	3.0	N
4-Oct-2008	16:00	2.6	N
4-Oct-2008	17:00	2.6	N
4-Oct-2008	18:00	2.2	NNE
4-Oct-2008	19:00	2.0	ENE
4-Oct-2008	20:00	1.9	WNW
4-Oct-2008	21:00	1.8	S
4-Oct-2008	22:00	2.4	WSW
4-Oct-2008	23:00	2.2	WSW
5-Oct-2008	00:00	2.1	W
5-Oct-2008	01:00	2.5	W
5-Oct-2008	02:00	2.3	WSW
5-Oct-2008	03:00	2.0	WSW
5-Oct-2008	04:00	2.3	WSW
5-Oct-2008	05:00	2.3	W
5-Oct-2008	06:00	2.4	W
5-Oct-2008	07:00	2.9	N
5-Oct-2008	08:00	2.7	W
5-Oct-2008	09:00	2.9	WNW
5-Oct-2008	10:00	2.8	ESE
5-Oct-2008	11:00	2.6	ESE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
5-Oct-2008	12:00	2.4	NE
5-Oct-2008	13:00	2.7	W
5-Oct-2008	14:00	3.2	NW
5-Oct-2008	15:00	3.2	WNW
5-Oct-2008	16:00	3.1	SSW
5-Oct-2008	17:00	2.6	W
5-Oct-2008	18:00	2.3	WNW
5-Oct-2008	19:00	1.9	WSW
5-Oct-2008	20:00	2.2	W
5-Oct-2008	21:00	2.2	WNW
5-Oct-2008	22:00	2.5	WNW
5-Oct-2008	23:00	2.5	N
6-Oct-2008	00:00	2.4	WNW
6-Oct-2008	01:00	3.0	N
6-Oct-2008	02:00	3.0	ENE
6-Oct-2008	03:00	3.0	NNE
6-Oct-2008	04:00	2.9	N
6-Oct-2008	05:00	2.8	WNW
6-Oct-2008	06:00	2.8	WNW
6-Oct-2008	07:00	2.5	WNW
6-Oct-2008	08:00	2.7	WNW
6-Oct-2008	09:00	2.6	WNW
6-Oct-2008	10:00	2.7	WNW
6-Oct-2008	11:00	3.4	W
6-Oct-2008	12:00	3.3	W
6-Oct-2008	13:00	3.0	W
6-Oct-2008	14:00	2.9	W
6-Oct-2008	15:00	3.0	WNW
6-Oct-2008	16:00	2.7	WNW
6-Oct-2008	17:00	2.9	WNW
6-Oct-2008	18:00	2.6	WNW
6-Oct-2008	19:00	2.6	WNW
6-Oct-2008	20:00	2.7	WNW
6-Oct-2008	21:00	2.0	WNW
6-Oct-2008	22:00	2.3	WNW
6-Oct-2008	23:00	1.9	WNW
7-Oct-2008	00:00	2.4	WNW
7-Oct-2008	01:00	2.6	WNW
7-Oct-2008	02:00	2.8	SW
7-Oct-2008	03:00	2.8	ENE
7-Oct-2008	04:00	3.0	ENE
7-Oct-2008	05:00	2.8	NNE
7-Oct-2008	06:00	2.7	SW
7-Oct-2008	07:00	3.0	SSW
7-Oct-2008	08:00	3.1	WNW
7-Oct-2008	09:00	3.2	WSW
7-Oct-2008	10:00	3.7	W
7-Oct-2008	11:00	3.7	WSW
7-Oct-2008	12:00	3.6	WSW
7-Oct-2008	13:00	3.4	WSW
7-Oct-2008	14:00	3.1	WSW
7-Oct-2008	15:00	3.3	ENE
7-Oct-2008	16:00	3.0	WSW
7-Oct-2008	17:00	3.3	SW

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
7-Oct-2008	18:00	2.8	SW
7-Oct-2008	19:00	2.8	SW
7-Oct-2008	20:00	2.4	NE
7-Oct-2008	21:00	2.1	W
7-Oct-2008	22:00	2.4	S
7-Oct-2008	23:00	3.3	SSW
8-Oct-2008	00:00	3.4	WSW
8-Oct-2008	01:00	3.4	SW
8-Oct-2008	02:00	3.3	SW
8-Oct-2008	03:00	3.2	SW
8-Oct-2008	04:00	3.6	SW
8-Oct-2008	05:00	3.8	NE
8-Oct-2008	06:00	3.2	WSW
8-Oct-2008	07:00	3.6	SW
8-Oct-2008	08:00	3.6	SSW
8-Oct-2008	09:00	3.0	NE
8-Oct-2008	10:00	2.0	NE
8-Oct-2008	11:00	2.8	N
8-Oct-2008	12:00	3.5	N
8-Oct-2008	13:00	2.7	E
8-Oct-2008	14:00	3.0	N
8-Oct-2008	15:00	2.9	N
8-Oct-2008	16:00	3.0	N
8-Oct-2008	17:00	2.9	N
8-Oct-2008	18:00	2.6	NNE
8-Oct-2008	19:00	2.3	NNE
8-Oct-2008	20:00	2.1	ENE
8-Oct-2008	21:00	1.6	N
8-Oct-2008	22:00	1.6	NNE
8-Oct-2008	23:00	1.7	N
9-Oct-2008	00:00	1.5	E
9-Oct-2008	01:00	1.7	NNE
9-Oct-2008	02:00	1.3	NE
9-Oct-2008	03:00	2.1	NE
9-Oct-2008	04:00	1.9	NE
9-Oct-2008	05:00	2.0	NE
9-Oct-2008	06:00	1.5	NE
9-Oct-2008	07:00	1.9	NE
9-Oct-2008	08:00	2.5	NE
9-Oct-2008	09:00	2.4	NE
9-Oct-2008	10:00	2.2	NE
9-Oct-2008	11:00	2.4	N
9-Oct-2008	12:00	2.4	N
9-Oct-2008	13:00	2.2	N
9-Oct-2008	14:00	2.2	E
9-Oct-2008	15:00	2.1	E
9-Oct-2008	16:00	2.4	E
9-Oct-2008	17:00	1.8	ENE
9-Oct-2008	18:00	1.8	NE
9-Oct-2008	19:00	1.6	NE
9-Oct-2008	20:00	1.3	ENE
9-Oct-2008	21:00	1.8	NE
9-Oct-2008	22:00	2.1	ENE
9-Oct-2008	23:00	1.3	NE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
10-Oct-2008	00:00	1.3	ENE
10-Oct-2008	01:00	1.7	ENE
10-Oct-2008	02:00	1.3	ENE
10-Oct-2008	03:00	1.4	ENE
10-Oct-2008	04:00	1.4	NNE
10-Oct-2008	05:00	1.4	NNE
10-Oct-2008	06:00	1.7	N
10-Oct-2008	07:00	1.1	NE
10-Oct-2008	08:00	0.8	N
10-Oct-2008	09:00	1.0	NE
10-Oct-2008	10:00	1.7	NNE
10-Oct-2008	11:00	1.4	ENE
10-Oct-2008	12:00	1.0	N
10-Oct-2008	13:00	1.6	NNE
10-Oct-2008	14:00	1.8	N
10-Oct-2008	15:00	1.9	NNE
10-Oct-2008	16:00	1.9	ENE
10-Oct-2008	17:00	2.4	NE
10-Oct-2008	18:00	1.7	S
10-Oct-2008	19:00	1.2	SE
10-Oct-2008	20:00	1.1	SE
10-Oct-2008	21:00	1.1	SE
10-Oct-2008	22:00	1.6	SE
10-Oct-2008	23:00	0.8	SE
11-Oct-2008	00:00	1.8	SW
11-Oct-2008	01:00	1.0	WSW
11-Oct-2008	02:00	0.8	SE
11-Oct-2008	03:00	1.4	SE
11-Oct-2008	04:00	1.4	SE
11-Oct-2008	05:00	1.3	ESE
11-Oct-2008	06:00	1.6	SSW
11-Oct-2008	07:00	1.3	SW
11-Oct-2008	08:00	1.4	ENE
11-Oct-2008	09:00	2.1	SE
11-Oct-2008	10:00	1.7	SE
11-Oct-2008	11:00	2.0	NE
11-Oct-2008	12:00	2.2	ENE
11-Oct-2008	13:00	2.2	ENE
11-Oct-2008	14:00	2.7	ENE
11-Oct-2008	15:00	2.9	NE
11-Oct-2008	16:00	2.8	NE
11-Oct-2008	17:00	3.8	NE
11-Oct-2008	18:00	2.4	ENE
11-Oct-2008	19:00	2.5	ENE
11-Oct-2008	20:00	2.1	NNE
11-Oct-2008	21:00	2.0	N
11-Oct-2008	22:00	2.0	N
11-Oct-2008	23:00	1.7	W
12-Oct-2008	00:00	1.4	N
12-Oct-2008	01:00	1.2	N
12-Oct-2008	02:00	1.3	N
12-Oct-2008	03:00	1.3	N
12-Oct-2008	04:00	1.0	N
12-Oct-2008	05:00	1.6	NE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
12-Oct-2008	06:00	1.6	NE
12-Oct-2008	07:00	1.6	ENE
12-Oct-2008	08:00	1.3	ENE
12-Oct-2008	09:00	2.0	ENE
12-Oct-2008	10:00	2.4	NE
12-Oct-2008	11:00	2.1	NNE
12-Oct-2008	12:00	2.3	ENE
12-Oct-2008	13:00	2.3	ENE
12-Oct-2008	14:00	2.4	E
12-Oct-2008	15:00	2.5	E
12-Oct-2008	16:00	2.4	E
12-Oct-2008	17:00	2.2	E
12-Oct-2008	18:00	2.0	E
12-Oct-2008	19:00	1.4	ENE
12-Oct-2008	20:00	1.0	ENE
12-Oct-2008	21:00	0.7	E
12-Oct-2008	22:00	1.2	ENE
12-Oct-2008	23:00	1.4	NNE
13-Oct-2008	00:00	1.1	NE
13-Oct-2008	01:00	1.2	N
13-Oct-2008	02:00	1.1	N
13-Oct-2008	03:00	1.2	ENE
13-Oct-2008	04:00	2.0	ENE
13-Oct-2008	05:00	1.4	ENE
13-Oct-2008	06:00	1.5	ENE
13-Oct-2008	07:00	1.4	NE
13-Oct-2008	08:00	1.7	NE
13-Oct-2008	09:00	2.6	S
13-Oct-2008	10:00	2.7	E
13-Oct-2008	11:00	2.8	E
13-Oct-2008	12:00	3.0	E
13-Oct-2008	13:00	2.6	ENE
13-Oct-2008	14:00	3.0	NE
13-Oct-2008	15:00	3.3	NE
13-Oct-2008	16:00	2.8	ENE
13-Oct-2008	17:00	2.7	NE
13-Oct-2008	18:00	2.5	ENE
13-Oct-2008	19:00	2.4	NE
13-Oct-2008	20:00	2.0	ENE
13-Oct-2008	21:00	1.2	ENE
13-Oct-2008	22:00	1.8	ENE
13-Oct-2008	23:00	1.6	E
14-Oct-2008	00:00	1.4	NE
14-Oct-2008	01:00	1.4	ENE
14-Oct-2008	02:00	1.4	NE
14-Oct-2008	03:00	1.6	E
14-Oct-2008	04:00	2.0	E
14-Oct-2008	05:00	1.6	ENE
14-Oct-2008	06:00	1.7	ENE
14-Oct-2008	07:00	1.8	ENE
14-Oct-2008	08:00	2.3	NE
14-Oct-2008	09:00	2.4	NE
14-Oct-2008	10:00	2.6	ENE
14-Oct-2008	11:00	3.1	NE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
14-Oct-2008	12:00	3.5	NE
14-Oct-2008	13:00	3.5	ENE
14-Oct-2008	14:00	3.7	SSE
14-Oct-2008	15:00	3.3	S
14-Oct-2008	16:00	3.4	SSE
14-Oct-2008	17:00	2.9	SE
14-Oct-2008	18:00	2.5	SE
14-Oct-2008	19:00	2.2	SE
14-Oct-2008	20:00	1.6	SE
14-Oct-2008	21:00	1.4	SE
14-Oct-2008	22:00	1.3	SW
14-Oct-2008	23:00	1.2	WSW
15-Oct-2008	00:00	1.5	WSW
15-Oct-2008	01:00	1.2	WSW
15-Oct-2008	02:00	2.0	SW
15-Oct-2008	03:00	1.8	NW
15-Oct-2008	04:00	2.1	NNW
15-Oct-2008	05:00	1.9	N
15-Oct-2008	06:00	1.9	N
15-Oct-2008	07:00	2.3	N
15-Oct-2008	08:00	2.4	NNW
15-Oct-2008	09:00	3.4	N
15-Oct-2008	10:00	3.4	N
15-Oct-2008	11:00	3.4	NNE
15-Oct-2008	12:00	3.6	E
15-Oct-2008	13:00	3.9	E
15-Oct-2008	14:00	3.7	SE
15-Oct-2008	15:00	3.9	SSE
15-Oct-2008	16:00	3.1	E
15-Oct-2008	17:00	2.4	WSW
15-Oct-2008	18:00	2.8	WNW
15-Oct-2008	19:00	1.7	NNW
15-Oct-2008	20:00	1.8	NNW
15-Oct-2008	21:00	1.6	N
15-Oct-2008	22:00	1.7	NNW
15-Oct-2008	23:00	1.7	NNE
16-Oct-2008	00:00	2.0	NE
16-Oct-2008	01:00	2.1	N
16-Oct-2008	02:00	2.2	NE
16-Oct-2008	03:00	2.2	NNE
16-Oct-2008	04:00	2.4	N
16-Oct-2008	05:00	2.7	N
16-Oct-2008	06:00	2.2	ESE
16-Oct-2008	07:00	2.7	NE
16-Oct-2008	08:00	1.9	ESE
16-Oct-2008	09:00	2.7	E
16-Oct-2008	10:00	3.2	NE
16-Oct-2008	11:00	2.4	NNE
16-Oct-2008	12:00	3.5	NE
16-Oct-2008	13:00	3.6	N
16-Oct-2008	14:00	3.6	NE
16-Oct-2008	15:00	3.6	NNE
16-Oct-2008	16:00	2.9	N
16-Oct-2008	17:00	2.6	NNE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
16-Oct-2008	18:00	3.2	N
16-Oct-2008	19:00	2.8	NNE
16-Oct-2008	20:00	1.5	ESE
16-Oct-2008	21:00	2.3	E
16-Oct-2008	22:00	2.0	NE
16-Oct-2008	23:00	2.0	SW
17-Oct-2008	00:00	2.1	SW
17-Oct-2008	01:00	2.0	SW
17-Oct-2008	02:00	2.2	SW
17-Oct-2008	03:00	2.5	SSW
17-Oct-2008	04:00	2.1	SW
17-Oct-2008	05:00	2.1	SSW
17-Oct-2008	06:00	1.7	S
17-Oct-2008	07:00	2.4	SSE
17-Oct-2008	08:00	2.5	SSW
17-Oct-2008	09:00	3.1	S
17-Oct-2008	10:00	3.0	SW
17-Oct-2008	11:00	2.7	SW
17-Oct-2008	12:00	2.5	WSW
17-Oct-2008	13:00	3.1	SW
17-Oct-2008	14:00	3.0	SW
17-Oct-2008	15:00	2.7	SW
17-Oct-2008	16:00	1.9	SW
17-Oct-2008	17:00	1.9	SSW
17-Oct-2008	18:00	2.4	SSW
17-Oct-2008	19:00	1.8	NE
17-Oct-2008	20:00	1.3	NE
17-Oct-2008	21:00	0.8	NE
17-Oct-2008	22:00	1.0	NE
17-Oct-2008	23:00	1.1	NNE
18-Oct-2008	00:00	0.9	NNE
18-Oct-2008	01:00	1.4	NE
18-Oct-2008	02:00	1.3	NE
18-Oct-2008	03:00	1.4	E
18-Oct-2008	04:00	1.4	ENE
18-Oct-2008	05:00	1.3	NNE
18-Oct-2008	06:00	1.2	SE
18-Oct-2008	07:00	1.1	SE
18-Oct-2008	08:00	1.1	SE
18-Oct-2008	09:00	1.5	S
18-Oct-2008	10:00	1.9	ESE
18-Oct-2008	11:00	2.0	N
18-Oct-2008	12:00	2.4	NNE
18-Oct-2008	13:00	3.3	SSE
18-Oct-2008	14:00	2.5	ESE
18-Oct-2008	15:00	2.9	NE
18-Oct-2008	16:00	2.3	SSE
18-Oct-2008	17:00	1.5	SE
18-Oct-2008	18:00	1.9	SSE
18-Oct-2008	19:00	2.3	SSE
18-Oct-2008	20:00	2.3	SSE
18-Oct-2008	21:00	2.1	SSE
18-Oct-2008	22:00	2.0	SSE
18-Oct-2008	23:00	2.2	ENE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
19-Oct-2008	00:00	2.3	ENE
19-Oct-2008	01:00	2.3	NNE
19-Oct-2008	02:00	2.4	NNE
19-Oct-2008	03:00	2.1	NNE
19-Oct-2008	04:00	1.7	SW
19-Oct-2008	05:00	1.5	NNE
19-Oct-2008	06:00	1.4	NE
19-Oct-2008	07:00	1.4	NE
19-Oct-2008	08:00	1.6	NE
19-Oct-2008	09:00	1.8	NE
19-Oct-2008	10:00	1.8	NE
19-Oct-2008	11:00	2.3	N
19-Oct-2008	12:00	2.6	NE
19-Oct-2008	13:00	2.5	N
19-Oct-2008	14:00	2.2	SE
19-Oct-2008	15:00	3.2	SE
19-Oct-2008	16:00	2.7	ENE
19-Oct-2008	17:00	2.8	E
19-Oct-2008	18:00	2.6	E
19-Oct-2008	19:00	2.3	E
19-Oct-2008	20:00	1.5	NE
19-Oct-2008	21:00	1.0	E
19-Oct-2008	22:00	1.9	E
19-Oct-2008	23:00	1.7	E
20-Oct-2008	00:00	1.4	SE
20-Oct-2008	01:00	1.3	SE
20-Oct-2008	02:00	1.4	ESE
20-Oct-2008	03:00	1.5	E
20-Oct-2008	04:00	1.6	SE
20-Oct-2008	05:00	2.0	SE
20-Oct-2008	06:00	2.3	SSE
20-Oct-2008	07:00	1.7	S
20-Oct-2008	08:00	1.4	S
20-Oct-2008	09:00	2.3	ENE
20-Oct-2008	10:00	2.1	E
20-Oct-2008	11:00	2.4	SE
20-Oct-2008	12:00	2.2	SE
20-Oct-2008	13:00	2.5	ESE
20-Oct-2008	14:00	2.2	E
20-Oct-2008	15:00	2.2	ESE
20-Oct-2008	16:00	2.1	NE
20-Oct-2008	17:00	2.4	NE
20-Oct-2008	18:00	2.0	E
20-Oct-2008	19:00	1.9	NNE
20-Oct-2008	20:00	1.3	NNE
20-Oct-2008	21:00	1.3	NE
20-Oct-2008	22:00	1.9	NE
20-Oct-2008	23:00	2.4	SE
21-Oct-2008	00:00	1.9	NE
21-Oct-2008	01:00	1.8	N
21-Oct-2008	02:00	1.9	ENE
21-Oct-2008	03:00	2.2	ENE
21-Oct-2008	04:00	1.6	NE
21-Oct-2008	05:00	2.3	NE



## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
21-Oct-2008	06:00	1.9	NE
21-Oct-2008	07:00	1.3	NNW
21-Oct-2008	08:00	1.5	N
21-Oct-2008	09:00	1.9	N
21-Oct-2008	10:00	2.5	N
21-Oct-2008	11:00	2.9	ENE
21-Oct-2008	12:00	3.6	ENE
21-Oct-2008	13:00	3.6	NNE
21-Oct-2008	14:00	3.3	NE
21-Oct-2008	15:00	3.4	E
21-Oct-2008	16:00	2.4	E
21-Oct-2008	17:00	2.4	ENE
21-Oct-2008	18:00	2.4	NE
21-Oct-2008	19:00	2.2	NE
21-Oct-2008	20:00	2.0	ENE
21-Oct-2008	21:00	2.0	ENE
21-Oct-2008	22:00	1.9	ENE
21-Oct-2008	23:00	2.0	ENE
22-Oct-2008	00:00	2.7	NNE
22-Oct-2008	01:00	1.8	NNE
22-Oct-2008	02:00	1.8	NNE
22-Oct-2008	03:00	2.0	N
22-Oct-2008	04:00	2.1	N
22-Oct-2008	05:00	1.7	NE
22-Oct-2008	06:00	1.8	SSW
22-Oct-2008	07:00	2.0	SW
22-Oct-2008	08:00	1.7	SW
22-Oct-2008	09:00	1.3	SSW
22-Oct-2008	10:00	1.5	SW
22-Oct-2008	11:00	2.2	SW
22-Oct-2008	12:00	2.9	SW
22-Oct-2008	13:00	3.1	SW
22-Oct-2008	14:00	3.4	W
22-Oct-2008	15:00	2.6	N
22-Oct-2008	16:00	2.2	NNW
22-Oct-2008	17:00	2.1	SW
22-Oct-2008	18:00	2.2	N
22-Oct-2008	19:00	2.0	WNW
22-Oct-2008	20:00	2.4	NE
22-Oct-2008	21:00	2.2	N
22-Oct-2008	22:00	1.4	N
22-Oct-2008	23:00	1.6	NNW
23-Oct-2008	00:00	1.6	N
23-Oct-2008	01:00	1.4	N
23-Oct-2008	02:00	1.3	N
23-Oct-2008	03:00	1.8	N
23-Oct-2008	04:00	1.8	N
23-Oct-2008	05:00	1.4	N
23-Oct-2008	06:00	1.4	N
23-Oct-2008	07:00	1.4	N
23-Oct-2008	08:00	1.3	N
23-Oct-2008	09:00	1.6	NNW
23-Oct-2008	10:00	2.4	E
23-Oct-2008	11:00	2.5	NNW

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
23-Oct-2008	12:00	2.5	WNW
23-Oct-2008	13:00	2.9	NNW
23-Oct-2008	14:00	2.9	NNW
23-Oct-2008	15:00	2.7	N
23-Oct-2008	16:00	2.7	NNW
23-Oct-2008	17:00	2.6	WSW
23-Oct-2008	18:00	3.1	SW
23-Oct-2008	19:00	2.9	N
23-Oct-2008	20:00	3.9	N
23-Oct-2008	21:00	3.4	ENE
23-Oct-2008	22:00	3.6	ENE
23-Oct-2008	23:00	3.4	ENE
24-Oct-2008	00:00	3.6	ENE
24-Oct-2008	01:00	3.5	ENE
24-Oct-2008	02:00	1.9	ENE
24-Oct-2008	03:00	2.2	SW
24-Oct-2008	04:00	3.1	SW
24-Oct-2008	05:00	3.2	SW
24-Oct-2008	06:00	3.1	SW
24-Oct-2008	07:00	3.4	SW
24-Oct-2008	08:00	2.6	ENE
24-Oct-2008	09:00	2.7	ENE
24-Oct-2008	10:00	2.8	ENE
24-Oct-2008	11:00	3.6	ENE
24-Oct-2008	12:00	3.7	ENE
24-Oct-2008	13:00	3.7	ENE
24-Oct-2008	14:00	3.3	ESE
24-Oct-2008	15:00	3.1	SSE
24-Oct-2008	16:00	3.5	SE
24-Oct-2008	17:00	2.2	SE
24-Oct-2008	18:00	1.5	S
24-Oct-2008	19:00	1.9	SSE
24-Oct-2008	20:00	1.7	SSE
24-Oct-2008	21:00	1.2	SSE
24-Oct-2008	22:00	1.4	SE
24-Oct-2008	23:00	1.8	SSE
25-Oct-2008	00:00	1.6	S
25-Oct-2008	01:00	1.8	S
25-Oct-2008	02:00	1.8	ENE
25-Oct-2008	03:00	1.0	NNE
25-Oct-2008	04:00	1.2	SW
25-Oct-2008	05:00	1.3	NE
25-Oct-2008	06:00	1.0	ESE
25-Oct-2008	07:00	0.8	ENE
25-Oct-2008	08:00	1.5	NE
25-Oct-2008	09:00	1.8	NE
25-Oct-2008	10:00	2.0	ENE
25-Oct-2008	11:00	3.0	ENE
25-Oct-2008	12:00	2.9	SW
25-Oct-2008	13:00	2.6	SW
25-Oct-2008	14:00	3.2	SW
25-Oct-2008	15:00	3.0	SW
25-Oct-2008	16:00	3.1	SSW
25-Oct-2008	17:00	2.8	ESE

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
25-Oct-2008	18:00	2.2	SSW
25-Oct-2008	19:00	2.3	SW
25-Oct-2008	20:00	1.9	ENE
25-Oct-2008	21:00	1.2	S
25-Oct-2008	22:00	1.4	S
25-Oct-2008	23:00	1.2	N
26-Oct-2008	00:00	1.0	NE
26-Oct-2008	01:00	1.0	WSW
26-Oct-2008	02:00	1.2	SW
26-Oct-2008	03:00	1.8	WSW
26-Oct-2008	04:00	1.0	WSW
26-Oct-2008	05:00	1.2	WSW
26-Oct-2008	06:00	1.1	SW
26-Oct-2008	07:00	1.2	SSW
26-Oct-2008	08:00	1.0	WSW
26-Oct-2008	09:00	1.4	SW
26-Oct-2008	10:00	1.7	ESE
26-Oct-2008	11:00	2.6	ESE
26-Oct-2008	12:00	2.4	NNE
26-Oct-2008	13:00	2.5	NNW
26-Oct-2008	14:00	2.4	N
26-Oct-2008	15:00	2.0	N
26-Oct-2008	16:00	2.6	NNE
26-Oct-2008	17:00	1.7	SW
26-Oct-2008	18:00	1.6	N
26-Oct-2008	19:00	1.5	SSE
26-Oct-2008	20:00	1.2	SW
26-Oct-2008	21:00	1.6	N
26-Oct-2008	22:00	2.0	ENE
26-Oct-2008	23:00	1.9	ENE
27-Oct-2008	00:00	2.3	ENE
27-Oct-2008	01:00	2.3	ENE
27-Oct-2008	02:00	1.8	ENE
27-Oct-2008	03:00	1.5	ENE
27-Oct-2008	04:00	1.8	NE
27-Oct-2008	05:00	1.5	ENE
27-Oct-2008	06:00	1.2	NE
27-Oct-2008	07:00	1.7	NE
27-Oct-2008	08:00	1.6	NE
27-Oct-2008	09:00	1.6	NE
27-Oct-2008	10:00	2.3	NE
27-Oct-2008	11:00	2.3	NNE
27-Oct-2008	12:00	2.7	N
27-Oct-2008	13:00	2.8	NNE
27-Oct-2008	14:00	3.0	N
27-Oct-2008	15:00	2.5	NNE
27-Oct-2008	16:00	2.7	NNW
27-Oct-2008	17:00	2.7	N
27-Oct-2008	18:00	2.5	N
27-Oct-2008	19:00	1.7	NNE
27-Oct-2008	20:00	1.4	N
27-Oct-2008	21:00	1.4	NE
27-Oct-2008	22:00	1.6	N
27-Oct-2008	23:00	1.9	N

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
28-Oct-2008	00:00	2.3	N
28-Oct-2008	01:00	2.1	N
28-Oct-2008	02:00	2.5	N
28-Oct-2008	03:00	1.9	N
28-Oct-2008	04:00	2.2	NNE
28-Oct-2008	05:00	1.7	N
28-Oct-2008	06:00	1.3	NE
28-Oct-2008	07:00	2.0	NE
28-Oct-2008	08:00	2.5	NE
28-Oct-2008	09:00	2.1	NE
28-Oct-2008	10:00	1.9	NE
28-Oct-2008	11:00	2.6	N
28-Oct-2008	12:00	2.3	N
28-Oct-2008	13:00	1.5	N
28-Oct-2008	14:00	1.8	N
28-Oct-2008	15:00	2.1	NNW
28-Oct-2008	16:00	1.5	NNW
28-Oct-2008	17:00	1.6	NNW
28-Oct-2008	18:00	1.7	N
28-Oct-2008	19:00	1.5	N
28-Oct-2008	20:00	1.4	N
28-Oct-2008	21:00	1.6	N
28-Oct-2008	22:00	1.4	SW
28-Oct-2008	23:00	2.0	SW
29-Oct-2008	00:00	1.8	SW
29-Oct-2008	01:00	1.8	SW
29-Oct-2008	02:00	1.9	SW
29-Oct-2008	03:00	2.6	SW
29-Oct-2008	04:00	1.3	WSW
29-Oct-2008	05:00	1.8	WSW
29-Oct-2008	06:00	1.5	SW
29-Oct-2008	07:00	0.8	SW
29-Oct-2008	08:00	0.8	SW
29-Oct-2008	09:00	0.6	W
29-Oct-2008	10:00	1.0	WNW
29-Oct-2008	11:00	1.5	SW
29-Oct-2008	12:00	1.3	SW
29-Oct-2008	13:00	1.7	SW
29-Oct-2008	14:00	1.6	NW
29-Oct-2008	15:00	2.3	SSW
29-Oct-2008	16:00	1.7	SSW
29-Oct-2008	17:00	1.6	SSW
29-Oct-2008	18:00	0.9	SW
29-Oct-2008	19:00	1.0	S
29-Oct-2008	20:00	1.1	N
29-Oct-2008	21:00	1.1	ENE
29-Oct-2008	22:00	1.6	ENE
29-Oct-2008	23:00	1.4	N
30-Oct-2008	00:00	1.4	NE
30-Oct-2008	01:00	1.3	NE
30-Oct-2008	02:00	1.5	NE
30-Oct-2008	03:00	1.5	NE
30-Oct-2008	04:00	1.3	NNE
30-Oct-2008	05:00	1.1	N

## Appendix J - Wind Data (Western Portal)

Date	Time	Wind Speed m/s	Direction
30-Oct-2008	06:00	1.0	N
30-Oct-2008	07:00	1.1	N
30-Oct-2008	08:00	1.3	N
30-Oct-2008	09:00	1.8	N
30-Oct-2008	10:00	2.0	N
30-Oct-2008	11:00	2.8	N
30-Oct-2008	12:00	3.5	N
30-Oct-2008	13:00	3.4	NNE
30-Oct-2008	14:00	3.6	NNE
30-Oct-2008	15:00	3.6	N
30-Oct-2008	16:00	3.3	NE
30-Oct-2008	17:00	2.8	NE
30-Oct-2008	18:00	2.2	NE
30-Oct-2008	19:00	1.8	NE
30-Oct-2008	20:00	2.0	NE
30-Oct-2008	21:00	1.5	NNE
30-Oct-2008	22:00	1.6	NNE
30-Oct-2008	23:00	1.1	N
31-Oct-2008	00:00	0.8	N
31-Oct-2008	01:00	1.0	NNE
31-Oct-2008	02:00	1.1	NNE
31-Oct-2008	03:00	1.0	ENE
31-Oct-2008	04:00	1.3	ENE
31-Oct-2008	05:00	1.2	ENE
31-Oct-2008	06:00	1.1	NNE
31-Oct-2008	07:00	0.9	NNE
31-Oct-2008	08:00	0.8	NE
31-Oct-2008	09:00	0.6	SSE
31-Oct-2008	10:00	0.6	SSE
31-Oct-2008	11:00	1.0	N
31-Oct-2008	12:00	1.1	NNE
31-Oct-2008	13:00	1.3	NE
31-Oct-2008	14:00	1.4	NNE
31-Oct-2008	15:00	1.3	ENE
31-Oct-2008	16:00	1.2	ENE
31-Oct-2008	17:00	1.2	N
31-Oct-2008	18:00	0.8	NNE
31-Oct-2008	19:00	0.7	N
31-Oct-2008	20:00	0.6	NNE
31-Oct-2008	21:00	0.6	N
31-Oct-2008	22:00	0.6	E
31-Oct-2008	23:00	0.5	E

---

**APPENDIX K  
SITE AUDIT SUMMARY**



---

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	81010
Date	10 October 2008 (Friday)
Time	9:00 – 10:00 and 13:45 – 16:15

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
81010-004	<ul style="list-style-type: none"> <li>Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.</li> </ul>	B15
	<b>B. Air Quality</b>	
81010-001	<ul style="list-style-type: none"> <li>Dark smoke was observed emitted from the generator at Western Portal. The Contractor was reminded to provide well maintenance for the plant equipments.</li> </ul>	D10
	<b>C. Noise</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>D. Waste / Chemical Management</b>	
81010-002	<ul style="list-style-type: none"> <li>Oil leakage was observed from the loader at Eastern Portal. The Contractor was reminded to clear them and well maintained the equipment.</li> </ul>	F8
	<b>E. Ecology</b>	
81010-003	<ul style="list-style-type: none"> <li>Milky water was observed discharging to the existing stream at Intake W3. The Contractor was reminded to provide mitigation measures to prevent any wastewater from running to the stream.</li> </ul>	G1
	<b>F. Marine Ecology</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>G. Reminders</b>	
81010-R05	<ul style="list-style-type: none"> <li>Clear all standing water I the label bag that secure around the trees at Eastern and Western Portal Sites.</li> </ul>	B15
	<b>H. Others</b>	
	<ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:80929), all environmental deficiencies were improved/rectified by contractor during the site inspection.</li> </ul>	



	Name	Signature	Date
Recorded by	Ivy Tam		10 October 2008
Checked by	Dr. Priscilla Choy		10 October 2008

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	81015
Date	15 October 2008 (Wednesday)
Time	11:00 – 12:00 and 13:00 – 18:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
81015-002	• Silty water was observed accumulate at the tank at Intake W3. The Contractor was reminded to clear them to prevent overflow during the rainstorm.	B15
81015-004	• Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.	B15
	<b>B. Air Quality</b>	
81015-003	• Dusty unpaved area was observed at Western Portal. The Contractor was reminded to provide water spray more frequently.	D5
	<b>C. Noise</b>	
81015-006	• Noise from water pump was noticed at Intake TP5. The Contractor was reminded to provide noise control measures to minimize noise nuisance.	E2
	<b>D. Waste / Chemical Management</b>	
81015-001	• Oil leakage was observed from the loader at Eastern Portal. The Contractor was reminded to clear them and well maintained the equipment.	F8
	<b>E. Ecology</b>	
81015-005	• Silty water was observed discharging to the existing stream at Intake TP4. The Contractor was reminded to provide mitigation measures to prevent any wastewater from running to the stream.	G1
	<b>F. Marine Ecology</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Reminders</b>	
81015-R07	• Clear all standing water in the label bag that secure around the trees at Eastern Portal, Western Portal and Intake sites.	B15
	<b>H. Others</b>	
	• Follow-up on previous audit section (Ref. No.:81010), all environmental deficiencies were improved/rectified by contractor except items (81010-002, 004 and R05). Follow-up action is needed for the outstanding items.	

	Name	Signature	Date
Recorded by	Ivy Tam		15 October 2008
Checked by	Dr. Priscilla Choy		15 October 2008





Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	81022
Date	22 October 2008 (Wednesday)
Time	14:45 – 18:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
81022-001	<ul style="list-style-type: none"> <li>Standing water was observed at the pit area at Intake TP4. The Contractor was reminded to dry it out.</li> </ul>	B15
	<b>B. Air Quality</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>C. Noise</b>	
81022-002	<ul style="list-style-type: none"> <li>Noise from water pump was noticed at Intake TP4. The Contractor was reminded to provide noise control measures to minimize noise nuisance.</li> </ul>	E2
	<b>D. Waste / Chemical Management</b>	
81022-003	<ul style="list-style-type: none"> <li>General refuses was observed at Intake TP5. The Contractor was reminded to clear them.</li> </ul>	F1iii.
81022-004	<ul style="list-style-type: none"> <li>Oil leakage with standing water at underneath of air compressor was observed at Western Portal. The Contractor was reminded to clear them properly.</li> </ul>	F8
81022-005	<ul style="list-style-type: none"> <li>Remaining oil was observed at the oil drum at Western Portal. The Contractor was reminded to clear them properly.</li> </ul>	F8
	<b>E. Ecology</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>F. Marine Ecology</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>G. Reminders</b>	
81022-R06	<ul style="list-style-type: none"> <li>Clear all standing water in the label bag that secure around the trees at Eastern Portal, Western Portal and Intake sites.</li> </ul>	B15
	<b>H. Others</b>	
	<ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:81015), all environmental deficiencies were improved/rectified by contractor except items (81015-O04 and R07). Follow-up action is needed for the outstanding items.</li> </ul>	

	Name	Signature	Date
Recorded by	Ivy Tam		22 October 2008
Checked by	Dr. Priscilla Choy		22 October 2008



**Contract No. DC/2007/10**  
**Design and Construction of Hong Kong West Drainage Tunnel**

**Weekly Site Inspection Record Summary**

**Inspection Information**

Checklist Reference Number	81030
Date	30 October 2008 (Thursday)
Time	13:00 – 17:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>A. Water Quality</b>	
81030-O02	• Leakage of water from the construction site at the bottom of hoarding at Eastern Portal was observed. The Contractor was reminded to seal the hoarding properly.	B5
81030-O03	• Stagnant water was observed at the pit area and drip tray at Eastern Portal. The Contractor was reminded to dry it out.	B15
81030-O06	• Drainage channel to nullah was observed accumulate with construction material. The Contractor was reminded to clear them.	B9
81030-O07	• Standing water with remaining oil was observed at underneath of air compressor at Western Portal. The Contractor was reminded to clear them properly.	B15
	<b>B. Air Quality</b>	
81030-O05	• Dry unpaved area was observed at Western Portal. The Contractor was reminded to provide water spray to control dust emission.	D5
	<b>C. Noise</b>	
81030-O01	• Noise from GI works was noticed at Intake RR1. The Contractor was reminded to provide noise control measures to minimize noise to the nearest residents.	E2
	<b>D. Waste / Chemical Management</b>	
81030-O07	• Standing water with remaining oil was observed at underneath of air compressor at Western Portal. The Contractor was reminded to clear them properly.	F8
	<b>E. Ecology</b>	
81030-O04	• Worm sand bags were observed at the access road at Eastern Portal near existing stream. The Contractor was reminded to replace them.	G1
	<b>F. Marine Ecology</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Reminders</b>	
81030-R09	• Keep clear the standing water in the label bags that secure around the trees at Eastern, Western and Intake sites.	B15
	<b>H. Others</b>	
81030-F08	• Follow-up on previous audit section (Ref. No.:81022), follow-up action is needed for the items (81022-O01-O05 and R06) as the Intakes P4 and TP5 were not observed during the site inspection.	

	Name	Signature	Date
Recorded by	Ivy Tam		30 October 2008
Checked by	Dr. Priscilla Choy		30 October 2008

---

**APPENDIX L  
ENVIRONMENTAL MITIGATION  
IMPLEMENTATION SCHEDULE (EMIS)**

---

## Appendix L - Summary of Environmental Mitigation Implementation Schedule

Types of Impacts	Mitigation Measures	Status
<b>Construction Dust</b>	<i>Dust Mitigation Measures</i>	
	<ul style="list-style-type: none"> <li>The Contractor shall undertake at all times to prevent dust nuisance as a result of his activities. Effective dust suppression measures should be installed to minimize air quality impacts, at the boundary of the site and at any sensitive receivers.</li> </ul>	^
	<ul style="list-style-type: none"> <li>No blasting shall be carried out when the strong wind signal or tropical cyclone warning signal No. 3 or higher is hoisted (unless prior permission of the Commissioner of Mines is obtained).</li> </ul>	^
	<ul style="list-style-type: none"> <li>Effective water sprays shall be used during the delivery and handling of all raw sand, aggregate and other similar materials, when dust is likely to be created, to dampen all stored materials during dry and windy weather. Watering of exposed surfaces shall be conducted as often as possible depending on the circumstances.</li> </ul>	*
	<ul style="list-style-type: none"> <li>A watering programme of once every 2 hours in normal weather conditions, and hourly in dry/windy conditions.</li> </ul>	*
	<ul style="list-style-type: none"> <li>Any stockpile of dusty material cannot be immediately transported out of the Site shall be either: a) covered entirely by impervious sheeting; b) placed in an area sheltered on the top and the three sides; or c) sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Should a conveyor system be used, the Contractor shall implement the following precautionary measures. Conveyor belts shall be fitted within windboards. Conveyor transfer points and hopper discharge areas shall be enclosed to minimize dust emission. All conveyors under control of the Contractor, and carrying materials which have the potential to create dust, shall be totally enclosed and fitted with belt cleaners.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Any dusty materials being discharged to vehicle from a conveying system at fixed transfer point, three-sided roofed enclosed with a flexible curtain across the entry shall be provided. Exhaust fans shall be provided for this enclosure and vented via a suitable fabric filter system.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>The heights from excavated spoils are dropped should be minimise to reduce the fugitive dust arising from unloading/loading.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The Contractor shall confine haulage and delivery vehicles to designated roadways inside the site. If in the opinion of the Engineer, any motorising vehicle is causing dust nuisance, the Engineer may require that the vehicle be restricted to a maximum speed of 15km per hour while within the site area.</li> </ul>	^
<ul style="list-style-type: none"> <li>Areas within the site where there is a regular movement of vehicles shall have an approved hard surface, be kept clear of loose surface materials and / or be regularly watered.</li> </ul>	^	
<ul style="list-style-type: none"> <li>Wheel cleaning facilities shall be installed for both portals and used by all vehicles leaving the site. No earth, mud, debris, dust and the like shall be deposited on public roads. Water in the wheel cleaning facility shall be changed at frequent intervals and sediments shall be removed regularly. The Contractor shall submit details of proposals for the wheel cleaning facilities to the Engineer prior to construction of the facility. Such wheel cleaning facilities shall be usable prior to any earthwork excavation activity on site. The Contractor shall provide a hard-surfaced road between any cleaning facility and the public road.</li> </ul>	^	
<ul style="list-style-type: none"> <li>Chemical wetting agents shall only be used on completed cuts and fills to reduce wind erosion.</li> </ul>	N/A	

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
 N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
 \* Recommendation was made during site audit but improved/rectified by the contractor;  
 # Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<ul style="list-style-type: none"> <li>• No vehicle exhausts shall be directed towards the ground or downwards to minimize dust nuisance.</li> <li>• Ventilation system, equipped with proprietary filters, should be provided to ensure the safe working environment inside the tunnel. Particular attention should be paid to the location and direction of the ventilation exhausts. The exhausts should not be allowed to face any sensitive receivers directly. Consideration should also be given to the location of windows, doors and direction of prevailing winds in relation to the nearby sensitive receivers.</li> <li>• In the event of any spoil or debris from construction works being deposited on adjacent land, or stream, or any silt being washed down to any area, then all such spoil, debris or material and silt shall be immediately removed and the affected land and areas restored to their natural state by the Contractor to the satisfaction of the Engineers.</li> </ul> <p>In addition, based on the <i>Air Pollution Control (Construction Dust) Regulation</i>, any works involved regulatory and notifiable works, such as stockpiling, loading and unloading of dusty materials, shall take precautions to suppress dust nuisance.</p> <ul style="list-style-type: none"> <li>• The working area of any excavation or earthmoving operation shall spray with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;</li> <li>• Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies; and</li> <li>• Any stockpile of dusty materials (greater than 20m<sup>3</sup>) shall be either covered entirely by impervious sheeting or placed in an area sheltered on the top and three sides; and sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.</li> <li>• Other suitable dust control measures as stipulated in <i>Air Pollution Control (Construction Dust) Regulation</i>, where appropriate, should be adopted.</li> </ul>	<p style="text-align: center;">*</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">*</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
<p><b>Construction Noise</b></p>	<p><u>Air borne noise</u></p> <p>In general, potential construction noise impact can be minimized or avoided by imposing a combination of the following mitigation measures:</p> <ul style="list-style-type: none"> <li>• Noisy equipment and activities should be sited by the Contractor as far from close-proximity sensitive receivers as practical. Prolonged operation of noisy equipment close to dwellings should be avoided.</li> <li>• The Contractor should minimise construction noise exposure to the schools (especially during examination periods). The Contractor should liaise with the school and the Examination Authority to ascertain the exact dates and times of all examination periods during the course of the works contract and to avoid noisy activities during these periods.</li> <li>• Noisy plant or processes should be replaced by quieter alternatives. Silenced diesel and gasoline generators and power units, as well as silenced and super-silenced air compressor, can be readily obtained.</li> <li>• Noisy activities should be scheduled to minimise exposure of nearby sensitive receivers to high levels of construction noise. For example, noisy activities can be scheduled for midday, or at times coinciding with periods of high background noise (such as during peak traffic hours).</li> <li>• Idle equipment should be turned off or throttled down. Noisy equipment should be properly maintained and used no more often than is necessary.</li> <li>• The power units of non-electric stationary plant and earth-moving plant should be quietened by vibration isolation and partial or full acoustic enclosures for individual noise-generating components.</li> <li>• Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided, thus reducing the cumulative impacts between operations. The numbers of operating items of powered mechanical equipment should be minimised. Noise can be reduced by increasing the distance between the operating equipment and the NSRs or by reducing the number of items of equipment and/or construction activity in the area at any one time.</li> <li>• The use of quiet plant working methods can further reduce noise level. Quiet plant is defined as Powered Mechanical Equipment (PME) whose actual sound power level is less than the value specified in the TMs for the same piece of equipment. To allow the Contractor some flexibility to select equipment to suit his needs, it is considered too restrictive to specify which specific items of silenced equipment to be used for the construction operations. It should be noted that various types of silenced equipment can be found in Hong Kong and are readily available on the market. BS 5228 also provides examples of quiet construction plant and their SWL.</li> <li>• Construction plant should be properly maintained (well-greased, damage and worn parts promptly replaced) and operated. Construction equipment often has silencing measures built in or added on, e.g. bulldozer silencers, compressor panels, and mufflers. Silencing measures should be properly maintained and utilised. Rubber or damping materials should be introduced between metal panels to avoid rattle and reverberation of noise.</li> <li>• Equipment known to emit sound strongly in one direction should be oriented so that the noise is directed away from nearby NSRs.</li> <li>• Materials stockpile and other structures (such as site offices) should be effectively utilised to shield construction noise. Noise</li> </ul>	<p>*</p> <p>^</p> <p>N/A</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>*</p> <p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p>can also be reduced by construction of temporary noise barriers which screen the lower floors from viewing the sites. Temporary noise barriers should be installed at active parts of construction areas where construction equipment is being operated in close proximity to NSRs.</p> <ul style="list-style-type: none"> <li>• It is noted that under the WBTC No. 19/2001, all construction sites are required to use metallic site hoarding can be slightly modified (with the addition of steel backings) into temporary noise barriers. These barriers should be gap free and have a surface mass density of at least 7kg/m<sup>2</sup>.</li> <li>• All hand-held percussive breakers and air compressors should comply the Noise Control (Hand-held Percussive Breakers) Regulations respectively under the NCO (Ordinance No. 75/88, NCO Amendment 1992 No.6).</li> </ul> <p>The Contractor shall devise, arrange methods of working and carry out the works in such manner as to minimise noise impacts on the surrounding environment, and shall provide experienced personnel with suitable training to ensure that these measures are implemented properly.</p> <p><u>Level 2 Use of Barriers</u></p> <p>Level 2 mitigation measures include providing movable barriers for sites which have sufficient space for installation, full enclosures during the drilling activities at Eastern Portal and at muck pit areas for Eastern portals and cantilever-typed high rise noise barrier for intake W5 (P) and W8.</p> <p>Before construction of the full enclosure at muck pit area, the use of full enclosure noise barrier (Stage A) for the drilling activities at the Eastern Portal area is required. A full enclosure for the muck pit area will then be constructed at this later stage (Stage B). The full enclosure shall be gap free apart from necessary entrance/exits, which shall face towards the entrance of eastern portal to minimize the amount of noise generated from affecting the nearest RNSRs especially school (True Light Middle School of Hong Kong).</p> <p>5m high cantilever-typed hoarding barrier to be built at W5 (P) and W8. These enclosures/barriers should have no gaps and have a superficial surface density of at least 10kg/m<sup>2</sup>. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period. To schedule the noise barrier erection and dismantling to the non sensitive periods of school to avoid adverse impact to W8/3.</p> <p>Movable barriers of 3 to 5m height with a small cantilevered upper portion and skid footing to be located within about 5 m or more for mobile equipment such that the line of sight is blocked. To provide purposes-built noise barriers or screens constructed of appropriate materials (minimum superficial density of 10kg/m<sup>2</sup>) located close to the operating PME.</p> <p>Pre-drilling following by chemical splitting instead of using large excavator mounted breaker should be used as mitigation measure for rock breaking and rock drilling.</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>N/A</p> <p>^</p> <p>^</p> <p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p>No construction activity is recommended during the examination period.</p> <p><u>Ground borne noise</u></p> <p>The noise level should be measured on the ground floor inside the nearest building during the TBM construction work in the daytime. If the daytime monitored ground borne noise exceeds the relevant evening/night ground borne noise criteria, evening/night construction work would not be carried out for the concerned tunnel section. Evening/night time construction work is subject to CNP application under the control of NCO.</p> <p>Public relationship strategy with 24-hour hotline system.</p>	<p>^</p> <p>N/A</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
 N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
 \* Recommendation was made during site audit but improved/rectified by the contractor;  
 # Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.



Types of Impacts	Mitigation Measures	Status
Water Quality	<u>Precautionary measures for construction work near natural streams</u>	
	<p>The government provides guidelines (ETWB TCW NO. 5/2005 and DSD TC 2/2004) are providing guidelines to minimize impacts when there is construction work carried out at near natural streams course. Relevant mitigation measures for the intakes are summarised as follows:</p>	
	<ul style="list-style-type: none"> <li>• Temporary site access to the work sites should be carefully planned and located to minimize disturbance caused to the substrates of streams/ivers and riparian vegetation by construction plant.</li> </ul>	^
	<ul style="list-style-type: none"> <li>• Locations well away from the rivers/streams for temporary storage of materials (e.g equipment, filling materials, chemicals and fuel) and temporary stockpile of construction debris and spoil should be identified before commencement of works.</li> </ul>	^
	<ul style="list-style-type: none"> <li>• Proposed works site areas inside, or in the proximity of, natural rivers and streams should be temporarily isolated to prevent adverse impacts on the stream water qualities.</li> </ul>	^
	<ul style="list-style-type: none"> <li>• Stockpiling of construction materials, if necessary, should be completely properly covered and located away from any natural stream/river.</li> </ul>	^
<ul style="list-style-type: none"> <li>• Construction debris and spoil should be covered up and/or properly disposed of as soon as possible to avoid being washed into nearby rivers/streams by rain and local runoff.</li> </ul>	^	
<u>Construction of temporary berthing point at the Western Portal</u>		
<p>A refuse collection vessel shall be provided to collect refuse or materials lost into the sea.</p>	^	
<p>The respective areas of the marine works will be completely enclosed by the silt curtain. The curtain shall be extended from water surface down to the seabed where it is anchored using sinker blocks. The Contractor shall inspect the silt curtain on regular basis to ensure its integrity and it is serviceable for all times.</p>	^	

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	Transfer of armour rock onto the seabed from barge at the temporary pier location should be conducted by careful grabbing and unloading to the seabed (to minimize sediment migration).	^
	The conveyor belt should be completely covered and muddy effluent from the temporary barge should be contained, treated and disposed. Where there is transfer of excavated wastes, the Contractor should provide appropriate measures to ensure that the waste is free from floatables, putrescibles, organic wastes and toxic materials and when required a refuse collection vessel be provided to collect float refuse.	N/A
	<u>Construction of stilling basin at Western Portal outfall</u>	
	All construction for the basin should be carried out inside the temporary cofferdam which is a temporary watertight enclosure built in the water and pumped dry to expose the bottom so that construction of stilling basin can be undertaken.	^
	During the dewatering process, appropriate desilting/sedimentation devices should be provided on site for treatment before discharge. The Contractor should ensure discharge water from the sedimentation tank meet the WPCO/TM requirements before discharge.	N/A
	The cofferdam will remain on site until after the construction of stilling basin has been completed. The coffer dam shall be regularly inspected and maintained to ensure no spillage of waste or wastewater into the sea. Conveyance of dredged materials from the coffer dam shall be carried out cautiously to avoid spillage into the sea.	N/A
	The filled material for the stilling basin should be contained inside the temporary cofferdam. The top level of the cofferdam shall be constructed higher than the final backfilled level.	^
	The Contractor shall be responsible for the design, installation and maintenance of the silt curtains to minimize the impacts on the water quality and the protection of water quality. The design and specification of the silt curtains shall be submitted by the Contractor to the Engineer for approval.	^
	Silt curtains shall be formed from tough, abrasion resistant, permeable membranes, suitable for the purpose, supported on floating booms in such a way as to ensure that the sediment plume shall be restricted to within the limit of the works area. The silt curtain shall be formed and installed in such a way that tidal rise and fall are accommodated, with the silt curtains always extending from the surface to the bottom of the water column and held with anchor blocks. The removal and reinstallation of such curtains during typhoon conditions shall be as agreed with the Director of Marine Department. The contractor shall regularly inspect the silt curtains and check that they are moored and marked to avoid danger to marine traffic. Any damage to the silt curtain shall be repaired by the Contractor promptly and the works shall be stopped until the repair is fixed to the satisfaction of the Engineer.	^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p>Transfer of rock fill material (armor rock) from the barge onto the site location should be conducted by grabbing and placement on the seabed to minimize sediment migration. No free dropping of the material will be allowed.</p>	^
	<p>Prior to the construction of armor rock based panel, a silt curtain shall also be installed prior to carry out any marine works as a preventive mitigation measure.</p>	^
	<p><u>Construction of TBM tunnel at both portals and intakes</u></p>	
	<p>Recycled water will be used at the cutter face for cooling purposes. Used water will be collected and discharged to a settling tank for settlement. Excess water from the settling tank will be transferred to the water treatment plant on site where the addition of flocculants will assist in settlement of solids. The Contractor should ensure discharge water from the sedimentation tank meet the WPCO/TM requirements before discharge.</p>	N/A
	<p>During the drilling process, all flushing water will be recycled for use. Discharge of the treated water to nearby drainage system shall be allowed provided that it has been treated to a level meeting with statutory requirements.</p>	^
	<p>Water flow at streams should be maintained by a temporary diversion system during the construction phase of intakes and manhole drop shafts.</p>	N/A
	<p><u>General Construction Activities and Workforce</u></p>	
	<p>A. Surface runoff</p>	
	<p>Effluent produced from construction activities are subjected to WPCO control. Effluent produced from sites should be diverted away from stream courses. Construction works near stream course should be scheduled in the dry season as far as practical to avoid excessive site runoff discharge.</p>	^
	<p>Under the <i>Water Pollution Control Ordinance</i> (WPCO), turbid water from construction sites must be treated to minimize the solids content before being discharged into storm drains. The suspended solids load can be reduced by directing the runoff into temporary sand traps or other silt-removal facilities, and other good and appropriate site management practices. Advice on the handling and disposal of construction site discharge is provided in the ProPECC Paper (PN 1/94) on Construction Site Drainage.</p>	^
	<p>A drainage system layout should be prepared by the Contractor for each of the works areas (portals and intakes), detailing the facilities and measures to manage pollution arising from surface runoff from those works areas. The drainage layout and an associated drainage management plan to reduce surface runoff sediments and pollutants entering watercourses, should be submitted to the Engineer for approval and to EPD for agreement.</p>	^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p>The system should be capable of handling stormwater from the site and directing it to sediment removal facilities before discharge. If oil and grease is used on the site or brought to the site, the stormwater should pass through oil interceptors before discharge. The interceptors should have a bypass to prevent washout in heavy storms.</p> <p>A temporary channel system or earth bunds or sand barriers should be provided in works areas on site to direct stormwater to silt-removal facilities. Stockpiled materials, if susceptible to erosion of rain or wind, should be covered with tarpaulins (or/similar fabric) or hydroseedings as far as practicable especially during the wet season.</p> <p>Silt removal facilities should be checked and the deposited silt and grit should be removed regularly to ensure these facilities are in good working condition and to prevent blockages.</p> <p>Vehicle washing areas should be drained into a settlement basin to settle out the suspended solid before discharge to storm water drains. The water should be recycled on site whenever possible. It is suggested that the wash water from the wheel wash basin is either reused for road watering or pumped to the on-site settling tanks for treatment. Water used for dust depression purposes should be minimized and an alternative soil holding agent should be considered.</p> <p><b>B. Spillage, Oil and Solvents</b>  Any contractor generating waste oil or other chemicals as a result of his activities should register as a chemical waste producer and provide a safe storage area for chemicals on site. Oil interceptors need to be regularly inspected and cleaned to avoid wash-out of oil during storm conditions. A bypass should be provided to avoid overload of the interceptor's capacity.</p> <p>Any spillage should be cleaned up immediately and the resulting contaminated absorbent material should be properly managed according to Waste Disposal Regulations. Spills should be contained to avoid spreading and contaminating the water resources.</p> <p>Oil and fuels should be used and stored properly in designated area. All fuel tanks and storage areas should be provided with locks and be sited on within sealed areas within surrounded by bunds of with a capacity equal to 110% of the storage capacity of the largest tank.</p> <p>Good housekeeping practices are required to minimize careless spillage and keep the work space in a tidy and clean condition. Appropriate training, including safety codes and relevant manuals, should be given to the personnel who regularly handle the chemicals on site.</p>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>*</p> <p>*</p> <p>*</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p>C. On-Site Effluent Generation</p> <p>Sewage arising from the additional population of workers on site should be collected in a suitable storage facility (chemical mobile toilets). Most of the work site locations are close to the public sewerage system, and therefore the use of septic tanks isare, therefore, not encouraged. Portable toilets should be used coupled with tickering away services provided by a licensed collector. They should be positioned at appropriate locations across the site to ensure no direct discharge of foul water off-site.</p> <p>D. Protection of Existing Flora and Fauna</p> <p>The Contractor should provide details of the plant and operation plans at each site for approval by the Engineer before commencing construction. The plans should include how the existing flora and fauna will be protected. Locations required for groundwater levels monitoring are Eastern Portal, PFLR1(P), THR2(P), TP5, TP789 and W12.</p> <p>The construction and demolition of the temporary pier may create short term impacts on the local marine water quality. The situation will be restored once the work is finished by proper phasing of the works programme and implementation of the adequate mitigation measures (e.g. silt curtain) the impacts will be minimized.</p> <p><u>Maintaining Baseflow in Downstream Watercourses</u></p> <p>The final design will be developed during the detailed design stage. The exact base flow rates to be maintained at each of the intakes will be subject to detailed site investigation at design stage.</p> <ul style="list-style-type: none"> <li>• Purpose of the by-pass device is to maintain the base-flow of the affected stream course.</li> <li>• The by-pass system comprises an approach link and a trapezoidal channel.</li> <li>• The approach link is section with inclined profiled surface at a gradient of 1 in 100. It is used to direct the base flow to the bypass trapezoidal channel at its down stream end during the normal days.</li> <li>• The trapezoidal channel is sized such that it could handle the base flow in the affected stream course which is estimated to be no more than 20 l/s.</li> <li>• Whenever the flow in the stream course exceeding the base flow rate, the excessive flow will overflow into the intake structure via the bottom rack structure. The bottom rack structure has bar screen on the top and inclined channel at the bottom. The top level of the bar screen is level with the by-pass channel with an aim to receive the overflow from the by-pass channel.</li> <li>• The by-pass channel is designed requiring minimum maintenance. However, it is recommended that the maintenance authority carry out regular maintenance inspection prior to onset of seasons and after significant rainstorm event to prevent blockage of the by-pass and bottom rack structure.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
<b>Waste/Chemical</b>	<p><u>General</u></p> <p>A proper waste management plan should be implemented to promote waste minimisation at source. Where waste generation is unavoidable then the potential for recycling or reuse should be explored and opportunities taken. If wastes cannot be recycled then the recommended disposal routes should be followed.</p>	*
	<p>All waste materials shall be segregated into categories covering:</p> <ul style="list-style-type: none"> <li>• Excavated material or construction waste suitable for reuse on-site</li> <li>• Excavated material or construction waste suitable for public filling areas</li> <li>• Remaining C&amp;D waste for landfill</li> <li>• Chemical waste, and</li> <li>• General refuse</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>
	<p>Proper segregation and disposal of construction waste should be implemented. Separate containers for inert and non-inert wastes should be provided. The inert waste should be taken to public filling area and the non-inert waste should be transported to strategic landfills.</p>	^
	<p>A trip-ticket system on the solid waste transfer/disposal operations should be included as one of the contractual requirements (ETWB TCW No. 31/2004). The Independent Environmental Checker (IEC) should be responsible for auditing this system.</p>	^
	<p>IEC should also be responsible for auditing the well-documented record system which includes: (i) quantity of waste generation, (ii) quantity of recycled material, (iii) quantity of disposed material, (iv) disposal methods and (v) sites should be implemented during construction phase.</p>	^
	<p>Regular cleaning and maintenance of the waste storage area should be conducted throughout the construction stage.</p>	^
	<p><u>Excavated spoil</u></p> <p>Control measures for soil temporarily stockpiled on-site should be taken in order to minimize the noise, generation of dust, pollution of water and visual impact. Key impacts include:</p>	^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.



Types of Impacts	Mitigation Measures	Status
<b>Terrestrial Ecology</b>	<p>During the detailed design stage, the following issues should also be considered as possible to further minimise the impacts:</p> <ul style="list-style-type: none"> <li>• Adjustment of site boundary to minimise temporary loss of natural stream habitat during construction.</li> <li>• Adjustment of site boundary to minimise use of mixed woodland as temporary works area. In particular, the woodland habitat in temporary works area of the Eastern Portal will be avoided, thereby greatly reducing the area of temporary loss of woodland habitat.</li> <li>• Minimizing felling of large trees.</li> <li>• About 20% of trees within the works area will be transplanted. The individual of <i>Artocarpus hypargyreus</i> recorded within the temporary works area of HKU1, if to be encroached, would also be transplanted.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p>
	<p>Standard site practices including the following, should be enforced to minimise the disturbance to the surroundings:</p> <ul style="list-style-type: none"> <li>• Treat any damage that may occur to large individual trees in the adjacent area using materials and methods appropriate for tree surgery.</li> <li>• Reinstate work sites/disturbed areas immediately after completion of the construction works, in particular, through on-site tree/shrub planting along the woodland and shrubland section within the temporary works area. Tree/shrub species used should make reference from those in the surrounding area.</li> <li>• Regularly check the work site boundaries to ensure that they are not exceeded and that no damage occurs to surrounding areas.</li> </ul>	<p>^</p> <p>^</p> <p>^</p>
	<p>A total of 1.02 ha would be replanted with woodland species, reaching almost a 1.5:1 ratio for compensatory planting. Tree/shrub species used should be based on those in the surrounding areas, including those which are commonly recorded during the baseline surveys.</p>	<p>^</p>
	<p>A low-flow channel would be provided within the channelised section to maintain a deeper water depth in the expanded channel, in particular during dry season as well as a basin at the end of the channelised section to provide living space for aquatic life. Step chute in the form of a series of descending water pools would be constructed between the low flow channel and the undisturbed stream course. There would also be openings for aquatic fauna between each chute step (pool). These could work like a “ladder” to help avoid isolating the aquatic fauna in the channelised section from natural habitats.</p>	<p>^</p>
	<p>Measures are also needed to maintain the flow of all affected streams/nullahs during the construction stages. Temporary bypass should be provided if the stream/nullah flows will be cut off by the construction works. After the construction works are finished, sections of temporary loss should be reinstated. Construction materials, wastes, and equipment should be cleared from the sites.</p>	<p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.



Types of Impacts	Mitigation Measures	Status
	<p>Surveys of amphibians at E4(P), PFLR1(P), W12(P), MB16, E5(B)(P), TP789(P) and P5(P) prior to commencement of construction is recommended. Frogs, including Hong Kong Cascade Frog and Lesser Spiny Frog, and tadpoles found at work areas of these proposed intake points will be collected and translocated to nearby streams that will not be affected by the project. These procedures should be performed by experienced herpetologists. A detailed translocation proposal will be submitted during the detailed design stage.</p> <p>Measures should also be taken to avoid runoff to streams and marine habitats. Stream/channel which could potentially be affected during construction should be prevented from sedimentation by erection of sediment barriers. Site runoff should be desilted by siltation traps in streams/channels or diverted, to reduce the potential for suspended sediments, organics and other contaminants to enter the local stream environment.</p>	<p>^</p> <p>^</p>
<b>Marine Ecology</b>	<p>Silt curtains will be deployed during the construction and demolition of the temporary berthing point. Deployment of silt curtains around the berthing point area would effectively avoid adverse water quality impacts due to barge filling. No significant ecological impact is anticipated.</p> <p>The invert of the stilling basin would be at -5.4 mPD. A cofferdam in the form of pipe-pile wall is to be constructed outside the stilling basin prior to the construction of basin. The cofferdam will be dewatered to provide a working area for construction of the stilling basin. The boulders from the seawall will then be removed by landbased grabs.</p> <p>Although the speed of the working vessels to be used in the Project (mainly barges) would not be high, a speed limit for marine traffic is proposed as a precautionary measure. A speed limit of 10 knots should be strictly enforced in the works area, in particular in the waters between the outfall location and the navigation channel in East Lamma Channel.</p>	<p>*</p> <p>N/A</p> <p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
Landscape and Visual	The proposed landscape and visual mitigation measures during the construction phase include:	
	CM1 - Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	^
	CM2 - Existing trees to be retained on site should be carefully protected during construction. The detailed proposal for any trees felling and transplantation is subject to Lands Department's approval on tree felling application at the detailed design stage.	^
	CM3 - Trees unavoidably affected by the works should be transplanted where practical.	^
	CM4 - Compensatory tree planting should be provided to compensate for felled trees.	^
	CM5 - The extent of disturbance on the existing stream course should be minimized. Any temporary works areas within the stream course shall be reinstated after construction.	^
	CM7 – Control of night-time lighting	^
	CM8 – Erection of decorative screen hoarding	^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
Cultural Heritage	<p>The Cultural Heritage Impact Assessment has identified the following resources which will require mitigation measures during the construction stage;</p>	
	<p><u>Haw Par Mansion (including boundary wall and gate)</u>  A condition survey must be undertaken by a qualified professional prior to the commencement of construction works for the tunnel portal in order to assess the structural integrity of the mansion, wall and gate (with special attention paid to any fragile architectural features). A report containing description of the types of construction, identification of fragile elements, an appraisal of the condition and a photographic record must be prepared. The report must also provide an assessment indicating whether further precautionary measures will be necessary during the construction phase, and if so provide details for sufficient protective measures, including monitoring for vibration control to ensure that no damage to the structure and fabric of the house, wall and gate results from the construction works. The report must be submitted to AMO for approval before construction activities commence. Upon approval the appropriate monitoring and precautionary measures shall be put into place.</p>	^
	<p>A buffer zone with a minimum width of 3 metres and an obstruction free access point must be maintained between the boundary wall/gate and the temporary works area (during construction works associated for both the tunnel portal and the permanent vehicle access ramp). This is to enable access for routine maintenance works on the wall and to ensure that the wall is not damaged by machinery operation or related construction activities. The temporary works area will be enclosed by standard DSD site hoarding.</p>	^
	<p><u>Former Explosive Magazine of Victoria Barracks</u>  A condition survey must be undertaken by a qualified professional prior to the commencement of construction works in order to assess the structural integrity of the retaining wall and the extent of damage from cracks and vegetation growth. A report containing a description of the wall's construction materials, identification of fragile and/or endangered elements, an appraisal of the condition and a photographic record of the retaining wall must be prepared. The report must also provide an assessment indicating whether further precautionary measures will be necessary during the construction phase, and if so provide details for sufficient protective measures, such as monitoring for vibration control, to ensure that no damage to the retaining wall results from the construction works. The report must be submitted to AMO for approval before construction activities commence. Upon approval the appropriate monitoring and precautionary measures shall be put into place.</p> <p>A buffer zone with a minimum width of 3 metres and an obstruction free access point must be maintained between the retaining wall and the temporary works area (for the duration of the construction phase). The works area will be enclosed by standard DSD site hoarding.</p>	^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
<b>Fisheries</b>	<p>Silt curtain will be deployed during the construction and demolition of the temporary berthing point. With the deployment of silt curtains around the berthing point area, adverse water quality impact associated with the filling would not be anticipated. No significant fisheries impact is anticipated.</p> <p>The invert of stilling basin will be found at -5.4 mPD. A cofferdam in the form of pipe-pipe wall is to be constructed outside the stilling basin prior to the construction of basin. The cofferdam will be dewatered to provide a working space for the construction of stilling basin. The boulders from the seawall will then be removed by landbased grabs.</p>	<p>^</p> <p>N/A</p>
<b>Hazard to Life</b>	<p>There will be no overnight storage of explosives for this project. Transportation of explosives to site for the construction of adit will be undertaken on a daily basis. The contractor is required to destroy any unused explosives before nightfall. If contractor wishes to set up magazines for overnight storage of explosives, it is necessary to carry out risk assessment and seek the relevant approval following the EIAO process.</p>	<p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

---

**APPENDIX M**  
**EVENT ACTION PLANS**

---

## Appendix M - Event Action Plans

### Event/Action Plan for Air Quality

EVENT	ACTION			
	ET	IEC	SUPERVISING OFFICER'S REPRESENTATIVE	CONTRACTOR
<b>ACTION LEVEL</b>				
1.Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify the source and investigate the causes and propose remedial measures</li> <li>2. Inform Supervising Officer's Representative &amp; IEC</li> <li>3. Repeat measurement to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET</li> <li>2.Check Contractor's working methods</li> </ol>	<ol style="list-style-type: none"> <li>1.Notify Contractor</li> </ol>	<ol style="list-style-type: none"> <li>1.Rectify any unacceptable practice</li> <li>2.Amend working methods if appropriate</li> </ol>
2.Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Identify the source</li> <li>2. Inform Supervising Officer's Representative &amp; IEC</li> <li>3. Repeat measurements to confirm findings</li> <li>4. Increase monitoring frequency to daily</li> <li>5. Discuss with Supervising Officer's Representative &amp; IEC for remedial actions required</li> <li>6. If exceedance continues, arrange meeting with Supervising Officer's Representative &amp; IEC</li> <li>7. If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1.Checking monitoring data submitted by ET</li> <li>2. Check Contractor's working methods</li> <li>3. Discuss with ET, IEC and Contractor on proposed remedial actions</li> <li>4. Advise the Supervising Officer's Representative &amp; ET on the effectiveness of the proposed remedial measures</li> <li>5.Supervise the implementation of the remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1.Confirm receipt of notification of failure in writing</li> <li>2.Notify Contractor</li> <li>3.Ensure remedial actions properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1.Submit proposals for remedial actions to Supervising Officer's Representative within 3 working days of notification</li> <li>2.Implement the agreed proposals</li> <li>3.Amend proposal if appropriate</li> </ol>
<b>LIMIT LEVEL</b>				
1.Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify source,,investigate the causes and propose remedial measures</li> <li>2. Inform Supervising Officer's Representative &amp; IEC and EPD</li> <li>3. Repeat measurement to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> <li>5. Assess effectiveness of Contractor's remedial actions and keep EPD and Supervising Officer's Representative &amp; IEC informed of the results</li> </ol>	<ol style="list-style-type: none"> <li>1.Check monitoring data submitted by ET</li> <li>2. Check Contractor's working methods</li> <li>3. Discuss with ET and Contractor on proposed remedial actions</li> <li>4. Advise the Supervising Officer's Representative on the effectiveness of the proposed remedial measures</li> <li>5.Supervise the implementation of the remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1.Confirm receipt of notification of failure in writing</li> <li>2.Notify Contractor</li> <li>3.Ensure remedial actions properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1.Take immediate action to avoid further exceedance</li> <li>2.Submit proposals for remedial actions to Supervising Officer's Representative within 3 working days of notification</li> <li>3.Implement the agreed proposals</li> <li>4.Amend proposal if appropriate</li> </ol>
2.Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Identify source</li> <li>2. Inform Supervising Officer's Representative, IEC and EPD the causes &amp; actions taken for the exceedances</li> <li>3. Repeat measurement to confirm findings</li> </ol>	<ol style="list-style-type: none"> <li>1.Discuss amongst Supervising Officer's Representative, ET and Contractor on the potential remedial actions</li> <li>2.Review Contractor's remedial actions to assure their effectiveness and advise the</li> </ol>	<ol style="list-style-type: none"> <li>1.Confirm receipt of notification of failure in writing</li> <li>2.Notify Contractor</li> <li>3.In consultation with the IEC, agree with the Contractor on the remedial measures to be</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Submit proposals for remedial actions to Supervising Officer's Representative within 3 working</li> </ol>

<b>ACTION</b>				
<b>EVENT</b>	<b>ET</b>	<b>IEC</b>	<b>SUPERVISING OFFICER'S REPRESENTATIVE</b>	<b>CONTRACTOR</b>
<b>ACTION LEVEL</b>				
	4. Increase monitoring frequency to daily 5. Investigate the causes of exceedance 6. Arrange meeting with & IEC and Supervising Officer's Representative to discuss the remedial actions to be taken 7. Assess effectiveness of Contractor's remedial actions and keep ER, IEC and EPD informed of the results 8. If exceedance stops, cease additional monitoring	Supervising Officer's Representative accordingly 3. Supervise the implementation of the remedial measures	implemented 4. Ensure remedial measure are properly implemented 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated	days of notification 3. Implement the agreed proposals 4. Resubmit proposals if problem still not under control 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	SUPERVISING OFFICER'S REPRESENTATIVE	Contractor
Action Level	<ol style="list-style-type: none"> <li>1. Notify IEC, Supervising Officer's Representative and Contractor</li> <li>2. carry our investigation by reviewing all the relevant monitoring data and the corresponding construction activities. Exceedances should also be confirmed by immediate verification in the field as far as practical.</li> <li>3. Report the results of investigation to the IEC, Supervising Officer's Representative and Contractor</li> <li>4. Discuss with the Contractor and formulate remedial measures</li> <li>5. increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analysed results submitted by the ET</li> <li>2. Review the proposed remedial measures by the Contractor and advise the Supervising Officer's Representative &amp; ET accordingly</li> <li>3. Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of complaint in writing</li> <li>2. Notify Contractor</li> <li>3. require Contractor to proposed remedial measures for analyzed noise problem</li> <li>4. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify practicable measures to minimize the noise impact. Submit noise mitigation proposals to ET, IEC and ET.</li> <li>2. Implement noise mitigation proposals</li> </ol>
Limit Level	<ol style="list-style-type: none"> <li>1. Notify IEC, Supervising Officer's Representative, EPD and Contractor</li> <li>2. Identify the source(s) of impact by reviewing all the relevant monitoring data and the corresponding construction activities. Exceedances should also be confirmed by immediate verification in the field as far as practical.</li> <li>3. Repeat measurement to confirm findings</li> <li>4. Increase monitoring frequency</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>6. inform IEC, Supervising Officer's Representative and EPD the cause &amp; actions taken for the exceedances</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and Supervising Officer's Representative informed of the results</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst Supervising Officer's Representative, ET, and Contractor on the potential remedial actions</li> <li>2. Review Contractor's remedial actions to assure their effectiveness and advise the Supervising Officer's Representative &amp; ET accordingly</li> <li>3. Supervise the implementation of the remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing</li> <li>2. Notify Contractor</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. If exceedance continuous, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is aborted</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Identify practicable measures to minimize the noise impact. Submit proposals for remedial actions to Supervising Officer's Representative within three working days of notification</li> <li>3. Implement the agreed proposals</li> <li>4. Resubmit proposal if problem still not under control</li> <li>5. Stop the relevant portion of works as determined by the Supervising Officer's Representative until the exceedance is abated</li> </ol>



Event/Action Plan for Water Quality

EVENT	ACTION			
	ET	IEC	SUPERVISING OFFICER'S REPRESENTATIVE	CONTRACTOR
<b>ACTION LEVEL</b>				
Action level being exceeded by one sampling day	<ol style="list-style-type: none"> <li>1. Repeat in situ measurement to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform IEC, contractor and Supervising Officer's Representative;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods.</li> <li>5. Discuss mitigation measures with IEC and Contractor</li> <li>6. Repeat measurement on next day of exceedance.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET and Contractor on the mitigation measures. Review proposals on mitigation measures submitted by Contractor and advise the Supervising Officer's Representative accordingly; and</li> <li>2. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IEC on the proposed mitigation measures; and</li> <li>2. Make agreement on the mitigation measures to be implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Supervising Officer's Representative and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with ET and IEC and propose mitigation measures to IEC and Supervising Officer's Representative;</li> <li>6. Implement the agreed mitigation measures.</li> </ol>
Action level being exceeded by more than one consecutive sampling days	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurement to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform IEC, contractor;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IEC, Supervising Officer's Representative and Contractor;</li> <li>6. Ensure mitigation measures are implemented;</li> <li>7. Prepare to increase the monitoring frequency to daily;</li> <li>8. Repeat measurement on next day of exceedance.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET and Contractor on the mitigation measures. Review proposals on mitigation measures submitted by Contractor and advise the Supervising Officer's Representative accordingly; and</li> <li>2. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IEC on the proposed mitigation measures; and</li> <li>2. Make agreement on the mitigation measures to be implemented.</li> <li>3. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Supervising Officer and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment and</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with ET and IEC and propose mitigation measures to IEC and Supervising Officer's Representative within 3 working days;</li> <li>6. Implement the agreed mitigation measures.</li> </ol>
<b>LIMIT LEVEL</b>				
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> <li>1. Repeat measurement on next of exceedance to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform IEC, contractor, Supervising Officer's Representative and EPD;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IEC, Supervising Officer's Representative and Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET and Contractor's working methods.</li> <li>2. Discuss with ET and Contractor on possible mitigation measures;</li> <li>3. Review the proposed mitigation measures submitted by Contractor and advise the Supervising Officer's Representative accordingly;</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Discuss with IEC, ET and Contractor on the proposed mitigation.</li> <li>3. Request Contractor to view the working methods.</li> <li>4. Ensure mitigation measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Supervising Officer's Representative and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment and consider changes of working methods;</li> <li>4. Discuss with ET, IEC and Supervising Officer's Representative and propose mitigation measures to Supervising Officer's Representative and IEC within 3 working days;</li> </ol>

EVENT	ACTION			
	ET	IEC	SUPERVISING OFFICER'S REPRESENTATIVE	CONTRACTOR
				5. Implement the agreed mitigation measures.
Limit level being exceeded by more than one consecutive sampling days	<ol style="list-style-type: none"> <li>1. Repeat measurement on next of exceedance to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform IEC, contractor, Supervising Officer's Representative and EPD;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IEC, Supervising Officer's Representative and Contractor;</li> <li>6. Ensure mitigation measures are implemented;</li> <li>7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET and Contractor's working methods.</li> <li>2. Discuss with ET and Contractor on possible mitigation measures;</li> <li>3. Review the proposed mitigation measures submitted by Contractor and advise the Supervising Officer's Representative accordingly;</li> <li>4. Supervise the implementation of mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>2. Request Contractor to critically review the working methods;</li> <li>3. Make agreement on the mitigation measures to be implemented;</li> <li>4. Ensure mitigation measures are properly implemented;</li> <li>5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Discuss with ET, IEC and Supervising Officer's Representative and propose mitigation measures to Supervising Officer's Representative and IEC within 3 working days;</li> <li>3. Implement the agreed mitigation measures;</li> <li>4. Resubmit proposals of mitigation measures if problem still not under control;</li> <li>5. As directed by the Supervising Officer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.</li> </ol>

---

**APPENDIX N  
COMPLAINT LOG**

---

**APPENDIX N – COMPLAINT LOG**

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
Com-2008-05-003	Construction site at Eastern Portal	22 May 2008	The complaint was lodged by Ms. Ng on 22 May 2008 regarding noise nuisance generated from the construction activities at the construction site of Eastern Portal	<p>According to the Contractor, only one excavator and one generator were operated for the excavation works around 8 am on 22 May 2008 at the Eastern portal. No other construction activities were conducted.</p> <p>In response to the complaint, The Contractor agreed to reschedule their current works activities, with immediate effect from 23 May 2008, that only site preparation works without noise nuisance to the nearby residents will be carried out from 7:00 am to 8:00 am at the Eastern Portal area.</p> <p>Base on the information collected and the monitoring results, the complaint was considered not justifiable since (1) no exceedance of the noise monitoring results was recorded in May and (2) no non-compliance or observation on noise was recorded.</p>	Closed
Com-2008-05-004	Construction site at Western Portal (Marine Works)	31 May 2008	The complaint was lodged by one of the local resident on 31 May 2008 regarding the noise nuisance generated from the marine works at Western Portal.	<p>According to the Contractor, only two derrick barges and one tug boat were operated for the seabed formation works around 18:00 hrs on 31 May 2008 at the Western Portal. No other construction activities were conducted.</p> <p>Base on the information collected and the monitoring results, the complaint was considered not justifiable since (1) no exceedance of the</p>	Closed

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
				noise monitoring results was recorded in May and (2) no non-compliance or observation on noise was recorded.	
Com-2008-07-007	Construction site at Eastern Portal	2 July 2008	The complaint was lodged by a resident of The Legend on 2 July 2008 regarding noise nuisance generated from the construction activities at the construction site of Eastern Portal	<p>According to the Contractor, only one generator and one drilling rig (Jumbo) were operated for the preparation works around 7:30a.m on 2 July 2008 at the Eastern portal. Construction noise was found from other construction site (Gammon Construction Limited) adjacent to Eastern Portal area.</p> <p>In response to the complaint, The Contractor review his forthcoming operations within the Eastern Portal site as previous they agreed, reschedule their current works activities, with immediate effect from 23 May 2008, that only site preparation works without noise nuisance to the nearby residents will be carried out from 7:00 am to 8:00 am at the Eastern Portal area.</p> <p>Additional noise monitoring was conducted on 16 and 17 July 2008 during the drilling rig (Jumbo), excavator and wheel loader were operated for drilling works.</p> <p>Base on the information collected and the monitoring results, the complaint was considered not justifiable since (1) no exceedance of the noise monitoring results was recorded in June and July 2008 and additional noise monitoring (2) no non-compliance or observation on noise was recorded.</p>	Closed

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
COM-2008-10-011	Construction site at Western Portal	11 October 2008	The complaint was lodged by one of the resident of Victoria Road, Ms Cheung on 11 October regarding about the noise nuisance generated from the construction works at Western Portal	<p>According to the Contractor, excavation works and marine works including sheet piling works were also conducted at the time of complaint at Western Portal</p> <p>Additional noise monitoring was conducted on 15 October 2008, drilling works, excavation works and marine works including sheet piling works were also conducted. The construction noise levels measured during the construction works were well below the construction noise limit of 75 dB(A)</p> <p>The Contractor agreed to reschedule the starting time of the construction works to 8:15am on every Saturday that without noise nuisance from the construction works to the nearby residents will be carried out from 7:00 am to 8:15 am at the Western Portal area.</p> <p>Base on the information collected, the noise level measured at outside Aegean Terrace during the construction works at Western Portal site were well below the construction noise limit of 75 dB(A). Also, the Contractor has implemented the remedial measure that reschedule the starting time of the construction works to 8:15am on every Saturday immediately after receiving the complaint to minimize the noise nuisance to the nearby residents.</p>	Closed
COM-2008-10-012	Construction site at Intake TP5	15 October 2008	The complaint was lodged by Mr Choi on 15 October 2008 regarding about the noise generated from the GI works, which starts from 8:30 hrs to	According to the information provided by the Contractor, only rotary type drill rigs and water pumps were operated for the GI works at the time of complaint at Intake TP5.	Closed

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
			17:30 hrs next to Aigburth at May Road.	Additional site inspection and noise monitoring at the podium of the Valverde at May Road were conducted on 3 Nov 2008 and 24 Oct, 5 Nov, 7 Nov 2008 respectively.	
COM-2008-10-013	Construction site at Intake TP5	31 October 2008	The complaint was lodged by Mr Lai on 31 October 2008 regarding the black smoke is emitted and noise is generated from the machine at the site (Intake TP5), he needed to close the windows to prevent the black smoke from entering his flat and to attenuate the noise.	<p>The Contractor agreed to reschedule the starting time of the construction works to 9:30am on every Saturday and 8:00 on normal weekdays that without noise nuisance to the nearby residents will be carried out from 7:00 am to 8:00 am at Intake TP5. Acoustic insulating materials have been applied for enclosing water pump and rotary type drill rigs to minimize the noise nuisance to the nearest residents.</p> <p>Base on the information collected, the noise level measured at the podium of the Valverde at May Road were well below the construction noise limit of 75 dB(A) after the Contractor has implemented the remedial measure.</p>	

---


**APPENDIX O**  
**CONSTRUCTION PROGRAMME**

---



Activity ID	Activity Description	Current or Forecast Duration	Current or Forecast Early Start	Current or Forecast Early Finish	Works Prog Total Float	Progress Total Float as of 21-Oct-08	% Comp	2008						2009
								JUL	AUG	SEP	OCT	NOV	DEC	JAN
<b>CC01 - PRELIMINARIES &amp; GENERAL REQUIREMENTS</b>														
<b>Milestone</b>														
<b>General</b>														
M1-1080	1.08-Complete of All Obligat's From 211to270d	0		01/SEP/08A	0		100							
M1-1090	1.09-Complete of All Obligat's From 271to300d	0		03/OCT/08A	0		100							
M1-1100	1.10-Complete of All Obligat's From 301to360d	0		03/OCT/08A	0		100							
M1-1380	1.38-Acceptance of Monthly Report on TDMS(9M)	0		01/SEP/08A	0		100							
M1-1390	1.39-Acceptance of Monthly Report on TDMS(10M)	0		03/OCT/08A	0		100							
M1-1400	1.40-Acceptance of Monthly Report on TDMS(11M)	0		30/OCT/08*	0	0	0							
M1-1410	1.41-Acceptance of Monthly Report on TDMS(12M)	0		29/NOV/08*	0	0	0							
M1-1420	1.42-Acceptance of Monthly Report on TDMS(13M)	0		30/DEC/08*	0	0	0							
<b>CC02 - DESIGN &amp; DESIGN CHECKING OF THE WORKS</b>														
<b>Design Stage</b>														
<b>Section 1 (Eastern Portal)</b>														
D00240	P&S East P Temp Drainage Divrsn Main Stream AIP	164	25/JUN/08A	25/SEP/08A	61		100							
D00245	APP East P Temp Drainage Divrsn Main Stream AIP	90	26/SEP/08A	24/DEC/08	61	97	25							
D00250	P&S East P Temp Drainage Divrsn Main Stream DDA	61	08/OCT/08A	07/DEC/08	21	24	21							
D00255	APP East P Temp Drainage Divrsn Main Stream DDA	90	08/DEC/08	07/MAR/09	21	24	0							
D00275	APP Cofferdam for Intake Shaft DDA	42	21/MAY/08A	27/OCT/08	-88	-206	90							
D00280	P&S Temp&Perm Supt EP Non-TBM Tuni to ch250 AIP	43	19/MAY/08A	12/SEP/08A	0		100							
D00282	APP Temp&Perm Supt EP Non-TBM Tuni to ch250 AIP	42	13/SEP/08A	27/OCT/08	0	-21	90							
D00283	P&S Temp Supt EP Non-TBM Tunnel to Ch250 - DDA	15	16/SEP/08A	28/OCT/08	0	-48	50							
D00284	APP Temp Supt EP Non-TBM Tunnel to Ch250 - DDA	30	29/OCT/08	27/NOV/08	0	-48	0							
D00286	P&S Perm Supt EP Non-TBM Tunnel to Ch250 - DDA	62	30/OCT/08*	30/DEC/08	504	504	0							
D00287	APP Perm Supt EP Non-TBM Tunnel to Ch250 - DDA	92	31/DEC/08	01/APR/09	504	504	0							
D00291	P&S EP Intake Tunnel&Intake Chamber Temp Sup AIP	15	13/MAY/08A	30/SEP/08A	0		100							
D00292	APP EP Intake Tunnel&Intake Chamber Temp Sup AIP	21	01/OCT/08A	21/OCT/08	0	-34	90							
D00293	P&S EP Intake Tunnel&Intake Chamber Temp Sup DDA	9	26/AUG/08A	30/SEP/08A	0		100							
D00294	APP EP Intake Tunnel&Intake Chamber Temp Sup DDA	20	01/OCT/08A	22/OCT/08	0	-30	90							
D00317	APP Boulder Assess Rep(EP)-inside Bound Stage 1	23	06/FEB/08A	27/OCT/08	-62	-215	90							
D00319	APP Boulder Assess Rep(EP)-outside Bound Stage 2	24	09/APR/08A	27/OCT/08	3	39	75							
D02334	APP East P Temp Drainage Divn Side Stream-DDA	76	28/MAR/08A	27/OCT/08	-19	-172	90							
D02344	P&S Temp Drain Divsn Main Stream ELS - AIP	81	10/JUN/08A	09/OCT/08A	0		100							
D02354	APP Temp Drain Divsn Main Stream ELS - AIP	42	10/OCT/08A	10/NOV/08	0	-31	25							
D02364	P&S Temp Drain Divsn Main Stream ELS - DDA	24	21/OCT/08*	13/NOV/08	0	-43	0							
D02374	APP Temp Drain Divsn Main Stream ELS - DDA	52	14/NOV/08	04/JAN/09	0	-43	0							
<b>Section 1 (Western Portal)</b>														
D00375	APP Temp Supp West Portal Soft Grd Tunnel DDA	42	12/JUN/08A	27/OCT/08	89	-15	90							
D00413	P&S Temp ELS WP Deep Struct (Basin)Single SP DDA	120	23/APR/08A	26/AUG/08A	0		100							
D00414	APP Temp ELS WP Deep Struct (Basin)Single SP DDA	21	27/AUG/08A	24/OCT/08	0	-39	90							
D00421	P&S Temp Suppt WP Hard Rd Tunnel(Arch shape)-AIP	15	29/AUG/08A	27/OCT/08	0	-42	75							
D00422	APP Temp Suppt WP Hard Rd Tunnel(Arch shape)-AIP	27	28/OCT/08	23/NOV/08	0	-42	0							
D00423	P&S Temp Suppt WP Hard Rd Tunnel(Arch shape)-DDA	15	11/SEP/08A	27/OCT/08	0	-33	90							
D00424	APP Temp Suppt WP Hard Rd Tunnel(Arch shape)-DDA	22	28/OCT/08	18/NOV/08	0	-33	0							
<b>Section 1 (Portion W0) - Dropshaft</b>														
D00630	P&S Dropshaft Temp Rock Supt (Excl. W0) AIP	70	13/OCT/08A	21/DEC/08	97	97	11							
D00633	APP Dropshaft Temp Rock Supt (Excl. W0) AIP	91	22/DEC/08	22/MAR/09	97	97	0							
D00642	P&S Dropshaft Permanent Lining (Excl W0) AIP	45	01/NOV/08*	15/DEC/08	132	132	0							
D00645	APP Dropshaft Permanent Lining (Excl W0) AIP	47	16/DEC/08	31/JAN/09	132	132	0							
D00654	P&S Dropshaft & SC at W0 Temp Rock Supt AIP	88	04/JUL/08A	10/NOV/08	48	6	93							
D00657	APP Dropshaft & SC at W0 Temp Rock Supt AIP	42	11/NOV/08	22/DEC/08	48	6	0							
D00660	P&S Dropshaft & SC at W0 Temp Rock Supt DDA	46	10/OCT/08A	14/NOV/08	2	2	48							
D00663	APP Dropshaft & SC at W0 Temp Rock Supt DDA	42	15/NOV/08	26/DEC/08	2	2	0							
<b>Section 1 (Portion W0)</b>														
D01145	APP W0-Permanent Works Intake AIP	64	18/JUL/08A	27/OCT/08	98	62	90							
D01150	P&S W0-Permanent Works Intake DDA	62	23/AUG/08A	10/NOV/08	831	805	62							
D01155	APP W0-Permanent Works Intake DDA	92	11/NOV/08	10/FEB/09	831	805	0							
D01156	P&S W0-Temp Works & Drainage Diversion AIP	49	08/MAY/08A	29/AUG/08A	126		100							
D01157	APP W0-Temp Works & Drainage Diversion AIP	92	30/AUG/08A	27/OCT/08	126	107	90							
D01158	P&S W0-Temp Works & Drainage Diversion DDA	62	27/AUG/08A	27/OCT/08	38	57	90							
D01159	APP W0-Temp Works & Drainage Diversion DDA	92	28/OCT/08	27/JAN/09	38	57	0							
<b>Section 7 (Portion THR2)</b>														
D00945	APP THR2-Permanent Works Intake AIP	92	08/AUG/08A	27/OCT/08	403	402	90							
D00956	P&S THR2-Temp Works & Drainage Diversion AIP	62	26/JUN/08A	23/SEP/08A	117		100							
D00957	APP THR2-Temp Works & Drainage Diversion AIP	92	24/SEP/08A	24/DEC/08	117	89	60							
<b>Section 4 (Portion MB16)</b>														
D00780	P&S MB16-Permanent Works Intake AIP	62	08/AUG/08A	11/OCT/08A	266		100							
D00785	APP MB16-Permanent Works Intake AIP	92	13/OCT/08A	12/JAN/09	266	262	13							
D00796	P&S MB16-Temp Works & Drainage Diversion - AIP	62	25/JUL/08A	11/OCT/08A	160		100							
D00797	APP MB16-Temp Works & Drainage Diversion - AIP	92	13/OCT/08A	12/JAN/09	160	149	21							
D00798	P&S MB16-Temp Works & Drainage Diversion - DDA	62	16/NOV/08*	16/JAN/09	145	145	0							
D00799	APP MB16-Temp Works & Drainage Diversion - DDA	92	17/JAN/09	18/APR/09	145	145	0							
D00820	P&S MB16-Permanent Slopeworks AIP	62	08/AUG/08A	06/OCT/08A	139		100							
D00825	APP MB16-Permanent Slopeworks AIP	122	07/OCT/08A	05/FEB/09	139	141	10							
D00826	P&S MB16-Permanent Slopeworks DDA	62	01/DEC/08*	31/JAN/09	938	1,023	0							
<b>Section 31 (Portion PFLR1)</b>														
D02250	P&S PFLR1-Permanent Works Intake AIP	64	30/JUN/08A	19/SEP/08A	290		100							
D02255	APP PFLR1-Permanent Works Intake AIP	92	20/SEP/08A	02/DEC/08	290	290	53							
D02266	P&S PFLR1-Temp Works & Drainage Diversion AIP	62	14/AUG/08A	12/NOV/08	61	33	63							
D02267	APP PFLR1-Temp Works & Drainage Diversion AIP	92	13/NOV/08	12/FEB/09	61	33	0							
<b>Section30 (Portion HKU1)</b>														
D02205	APP HKU1-Permanent Works Intake AIP	92	08/AUG/08A	27/OCT/08	458	457	94							
D02210	P&S HKU1-Permanent Works Intake DDA	62	02/OCT/08A	02/DEC/08	422	421	32							
D02215	APP HKU1-Permanent Works Intake DDA	92	03/DEC/08	04/MAR/09	422	421	0							
D02216	P&S HKU1-Temp Works & Drainage Diversion AIP	62	26/JUN/08A	23/SEP/08A	79		100							
D02217	APP HKU1-Temp Works & Drainage Diversion AIP	122	24/OCT/08A	23/JAN/09	79	51	22							
<b>Section 6 (Portion E7)</b>														
D00880	P&S E7 - Permanent Works Intake AIP	62	23/JUL/08A	19/SEP/08A	206		100							
D00885	APP E7 - Permanent Works Intake AIP	92	20/SEP/08A	20/DEC/08	206	232	33							
D00896	P&S E7 - Temp Works & Drainage Diversion - AIP	62	01/AUG/08A	29/OCT/08	220	192	85							
D00897	APP E7 - Temp Works & Drainage Diversion - AIP	92	30/OCT/08	29/JAN/09	220	192	0							
D00898	P&S E7 - Temp Works & Drainage Diversion - DDA	62	16/DEC/08*	15/FEB/09	175	175	0							

Start Date 23/NOV/07  
 Finish Date 22/MAR/12  
 Data Date 21/OCT/08  
 Run Date 25/OCT/08 14:52



810A  
 Design & Construction of Hong Kong West Drainage Tunnel  
 Contract No. DC/2007/10  
 Works Programme  
 3 Monthly Rolling Programme  
 OCT MONTHLY REPORT



Date	Revision	Checked	Approved
25/OCT/08	11th Monthly Update		
23/Sep08	21/Oct08		

Activity ID	Activity Description	Current or Forecast Duration	Current or Forecast Early Start	Current or Forecast Early Finish	Works Prog Total Float	Progress Total Float as of 21-Oct-08	% Comp	2008						2009			
								JUL	AUG	SEP	OCT	NOV	DEC	JAN			
								[Gantt Chart Area]									
D00920	P&S E7 - Permanent Slopeworks AIP	62	01/SEP/08A	09/OCT/08A	591		100										
D00925	APP E7 - Permanent Slopeworks AIP	122	10/OCT/08A	08/FEB/09	591	614	9										
D00930	P&S E7 - Permanent Slopeworks DDA	62	01/JAN/09*	03/MAR/09	591	591	0										
<b>Section 29 (Portion W10)</b>																	
D02150	P&S W10-Permanent Works Intake AIP	62	23/AUG/08A	03/NOV/08	430	411	75										
D02155	APP W10-Permanent Works Intake AIP	92	04/NOV/08	03/FEB/09	430	411	0										
D02166	P&S W10-Temp Works & Drainage Diversion AIP	62	29/SEP/08A	29/NOV/08	75	77	33										
D02167	APP W10-Temp Works & Drainage Diversion AIP	122	30/NOV/08	31/MAR/09	75	77	0										
<b>Section 32 (Portion SM1)</b>																	
D02300	P&S SM1-Permanent Works Intake AIP	62	30/JUN/08A	19/SEP/08A	270		100										
D02305	APP SM1-Permanent Works Intake AIP	92	20/SEP/08A	30/NOV/08	270	270	55										
D02310	P&S SM1-Permanent Works Intake DDA	63	01/NOV/08*	02/JAN/09	237	237	0										
D02315	APP SM1-Permanent Works Intake DDA	92	03/JAN/09	04/APR/09	237	237	0										
D02316	P&S SM1-Temp Works & Drainage Diversion AIP	62	25/JUL/08A	23/SEP/08A	238		100										
D02317	APP SM1-Temp Works & Drainage Diversion AIP	92	24/SEP/08A	01/JAN/09	238	238	29										
D02318	P&S SM1-Temp Works & Drainage Diversion DDA	62	22/DEC/08*	21/FEB/09	187	187	0										
<b>Section 26 (Portion RR1)</b>																	
D02000	P&S RR1-Permanent Works Intake AIP	62	08/OCT/08A	08/DEC/08	644	637	32										
D02005	APP RR1-Permanent Works Intake AIP	92	09/DEC/08	10/MAR/09	644	637	0										
D02016	P&S RR1-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	112	112	0										
D02017	APP RR1-Temp Works & Drainage Diversion AIP	122	02/JAN/09	03/MAY/09	204	204	0										
<b>Section 5 (Portion MBD2)</b>																	
D00830	P&S MBD2-Permanent Works Intake AIP	62	09/OCT/08A	09/DEC/08	274	266	32										
D00835	APP MBD2-Permanent Works Intake AIP	92	10/DEC/08	11/MAR/09	274	266	0										
D00850	P&S MBD2-Temp Works & Drainage Diversion AIP	62	16/OCT/08A	16/DEC/08	166	166	8										
D00855	APP MBD2-Temp Works & Drainage Diversion AIP	92	17/DEC/08	18/MAR/09	166	166	0										
<b>Section 23 (Portion TP4)</b>																	
D01840	P&S TP4-Permanent Works Intake AIP	62	16/AUG/08A	15/OCT/08A	358		100										
D01845	APP TP4-Permanent Works Intake AIP	92	13/OCT/08A	12/JAN/09	358	362	8										
D01856	P&S TP4-Temp Works & Drainage Diversion AIP	62	04/SEP/08A	01/NOV/08	190	190	80										
D01857	APP TP4-Temp Works & Drainage Diversion AIP	92	02/NOV/08	01/FEB/09	190	190	0										
D01880	P&S TP4-Permanent Slopeworks AIP	62	30/AUG/08A	01/NOV/08	130	130	80										
D01885	APP TP4-Permanent Slopeworks AIP	122	02/NOV/08	03/MAR/09	130	130	0										
<b>Section 28 (Portion P5)</b>																	
D02100	P&S P5-Permanent Works Intake AIP	62	03/SEP/08A	01/NOV/08	323	323	80										
D02105	APP P5-Permanent Works Intake AIP	92	02/NOV/08	01/FEB/09	323	323	0										
D02116	P&S P5-Temp Works & Drainage Diversion AIP	62	16/SEP/08A	16/NOV/08	248	248	56										
D02117	APP P5-Temp Works & Drainage Diversion AIP	122	17/NOV/08	18/MAR/09	248	248	0										
<b>Section 22 (Portion TP5)</b>																	
D01790	P&S TP5-Permanent Works Intake AIP	62	04/SEP/08A	01/NOV/08	426	426	80										
D01795	APP TP5-Permanent Works Intake AIP	92	02/NOV/08	01/FEB/09	426	426	0										
D01806	P&S TP5-Temp Works & Drainage Diversion AIP	62	23/SEP/08A	24/NOV/08	206	202	50										
D01807	APP TP5-Temp Works & Drainage Diversion AIP	92	25/NOV/08	24/FEB/09	206	202	0										
<b>Section 21 (Portion TP789)</b>																	
D01730	P&S TP789-Permanent Works Intake AIP	62	16/SEP/08A	01/DEC/08	295	295	32										
D01735	APP TP789-Permanent Works Intake AIP	92	02/DEC/08	03/MAR/09	295	295	0										
D01746	P&S TP789-Temp Works & Drainage Diversion AIP	62	04/SEP/08A	01/NOV/08	325	325	80										
D01747	APP TP789-Temp Works & Drainage Diversion AIP	92	02/NOV/08	01/FEB/09	325	325	0										
<b>Section 24 (Portion W5)</b>																	
D01904	P&S W5-Permanent Works Intake AIP	62	16/OCT/08A	16/DEC/08	496	496	8										
D01905	APP W5-Permanent Works Intake AIP	92	17/DEC/08	18/MAR/09	496	496	0										
D01910	P&S W5-Temp Works & Drainage Diversion AIP	63	01/NOV/08*	02/JAN/09	221	221	0										
D01911	APP W5-Temp Works & Drainage Diversion AIP	122	03/JAN/09	04/MAY/09	221	221	0										
D01912	P&S W5-Temp Works & Drainage Diversion DDA	62	16/JAN/09*	18/MAR/09	194	194	0										
<b>Section 2 (Portion E5A)</b>																	
D00680	P&S E5A-Permanent Works Intake AIP	62	19/SEP/08A	16/NOV/08	370	370	56										
D00682	APP E5A-Permanent Works Intake AIP	92	17/NOV/08	16/FEB/09	370	370	0										
D00687	P&S E5A-Temp Works & Drainage Diversion AIP	62	16/SEP/08A	17/OCT/08A	243		100										
D00688	APP E5A-Temp Works & Drainage Diversion AIP	92	18/OCT/08A	17/JAN/09	243	273	3										
<b>Section 27 (Portion W8)</b>																	
D02050	P&S W8-Permanent Works Intake AIP	62	08/OCT/08A	08/DEC/08	605	598	31										
D02055	APP W8-Permanent Works Intake AIP	92	09/DEC/08	10/MAR/09	605	598	0										
D02066	P&S W8-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	226	226	0										
D02067	APP W8-Temp Works & Drainage Diversion AIP	92	02/JAN/09	03/APR/09	226	226	0										
<b>Section 3 (Portion E5B)</b>																	
D00730	P&S E5B-Permanent Works Intake AIP	62	01/SEP/08A	11/OCT/08A	427		100										
D00735	APP E5B-Permanent Works Intake AIP	92	13/OCT/08A	12/JAN/09	427	447	8										
D00746	P&S E5B-Temp Works & Drainage Diversion AIP	62	09/SEP/08A	05/NOV/08	334	334	74										
D00747	APP E5B-Temp Works & Drainage Diversion AIP	92	06/NOV/08	05/FEB/09	334	334	0										
<b>Section 20 (Portion M3)</b>																	
D01670	P&S M3-Permanent Works Intake AIP	62	15/OCT/08A	14/DEC/08	306	293	9										
D01675	APP M3-Permanent Works Intake AIP	92	15/DEC/08	16/MAR/09	306	293	0										
D01686	P&S M3-Temp Works & Drainage Diversion AIP	62	08/OCT/08A	08/DEC/08	306	299	20										
D01687	APP M3-Temp Works & Drainage Diversion AIP	92	09/DEC/08	10/MAR/09	306	299	0										
D01710	P&S M3-Permanent Slopeworks AIP	62	08/OCT/08A	08/DEC/08	246	239	20										
D01715	APP M3-Permanent Slopeworks AIP	122	09/DEC/08	09/APR/09	246	239	0										
<b>Section 19 (Portion MA17)</b>																	
D01610	P&S MA17-Permanent Works Intake AIP	62	16/OCT/08A	16/DEC/08	252	252	8										
D01615	APP MA17-Permanent Works Intake AIP	92	17/DEC/08	18/MAR/09	252	252	0										
D01626	P&S MA17-Temp Works & Drainage Diversion AIP	63	01/NOV/08*	02/JAN/09	235	235	0										
D01627	APP MA17-Temp Works & Drainage Diversion AIP	92	03/JAN/09	04/APR/09	235	235	0										
D01650	P&S MA17-Permanent Slopeworks AIP	62	02/OCT/08A	02/DEC/08	269	268	30										
D01655	APP MA17-Permanent Slopeworks AIP	122	03/DEC/08	03/APR/09	269	268	0										
<b>Section 15 (Portion W3)</b>																	
D01400	P&S W3-Permanent Works Intake AIP	62	01/NOV/08*	01/JAN/09	472	472	0										
D01405	APP W3-Permanent Works Intake AIP	92	02/JAN/09	03/APR/09	472	472	0										
D01416	P&S W3-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	534	534	0										
D01417	APP W3-Temp Works & Drainage Diversion AIP	92	02/JAN/09	03/APR/09	534	534	0										
<b>Section 17 (Portion MA14)</b>																	
D01500	P&S MA14-Permanent Works Intake AIP	62	01/NOV/08*	01/JAN/09	413	413	0										
D01505	APP MA14-Permanent Works Intake AIP	92	02/JAN/09	03/APR/09	413	413	0										
D01516	P&S MA14-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	344	344	0										

Start Date: 23/NOV/07  
 Finish Date: 22/MAR/12  
 Data Date: 21/OCT/08  
 Run Date: 25/OCT/08 14:52

Target Bar  
 Progress Bar  
 Critical Activity

810A  
 Sheet 2 of 6  
 Design & Construction of Hong Kong  
 West Drainage Tunnel  
 Contract No. DC/2007/10  
 Works Programme  
 3 Monthly Rolling Programme  
 OCT MONTHLY REPORT

Activity ID	Activity Description	Current or Forecast Duration	Current or Forecast Early Start	Current or Forecast Early Finish	Works Prog Total Float	Progress Total Float as of 21-Oct-08	% Comp	2008						2009
								JUL	AUG	SEP	OCT	NOV	DEC	JAN
D01517	APP MA14-Temp Works & Drainage Diversion AIP	92	02/JAN/09	03/APR/09	344	344	0							
D01540	P&S MA14-Permanent Slopeworks AIP	62	01/NOV/08*	01/JAN/09	323	323	0							
D01545	APP MA14-Permanent Slopeworks AIP	122	02/JAN/09	03/MAY/09	323	323	0							
<b>Section 18 (Portion MA15)</b>														
D01560	P&S MA15-Permanent Works Intake AIP	62	01/NOV/08*	01/JAN/09	402	402	0							
D01565	APP MA15-Permanent Works Intake AIP	92	02/JAN/09	03/APR/09	402	402	0							
D01580	P&S MA15-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	286	286	0							
D01585	APP MA15-Temp Works & Drainage Diversion AIP	92	02/JAN/09	03/APR/09	286	286	0							
<b>Section 10 (Portion DG1)</b>														
D01090	P&S DG1-Permanent Works Intake AIP	62	16/OCT/08A	16/DEC/08	350	350	8							
D01095	APP DG1-Permanent Works Intake AIP	92	17/DEC/08	18/MAR/09	350	350	0							
D01106	P&S DG1-Temp Works & Drainage Diversion AIP	62	16/OCT/08A	16/DEC/08	319	319	8							
D01107	APP DG1-Temp Works & Drainage Diversion AIP	92	17/DEC/08	18/MAR/09	319	319	0							
<b>Section 9 (Portion HR1)</b>														
D01040	P&S HR1-Permanent Works Intake AIP	62	19/SEP/08A	16/NOV/08	607	607	56							
D01045	APP HR1-Permanent Works Intake AIP	92	17/NOV/08	16/FEB/09	607	607	0							
D01056	P&S HR1-Temp Works & Drainage Diversion AIP	62	16/NOV/08*	16/JAN/09	348	348	0							
D01057	APP HR1-Temp Works & Drainage Diversion AIP	92	17/JAN/09	18/APR/09	348	348	0							
<b>Section 14 (Portion BR6)</b>														
D01350	P&S BR6-Permanent Works Intake AIP	62	16/NOV/08*	16/JAN/09	365	365	0							
D01355	APP BR6-Permanent Works Intake AIP	92	17/JAN/09	18/APR/09	365	365	0							
D01370	P&S BR6-Temp Works & Drainage Diversion AIP	62	16/NOV/08*	16/JAN/09	302	302	0							
D01375	APP BR6-Temp Works & Drainage Diversion AIP	92	17/JAN/09	18/APR/09	302	302	0							
<b>Section 12 (Portion W1)</b>														
D01250	P&S W1-Permanent Works Intake AIP	62	16/OCT/08A	16/DEC/08	404	404	8							
D01255	APP W1-Permanent Works Intake AIP	92	17/DEC/08	18/MAR/09	404	404	0							
D01266	P&S W1-Temp Works & Drainage Diversion AIP	62	01/NOV/08*	01/JAN/09	396	396	0							
D01267	APP W1-Temp Works & Drainage Diversion AIP	92	02/JAN/09	03/APR/09	396	396	0							
<b>Section 8 (Portion GL1)</b>														
D00990	P&S GL1-Permanent Works Intake AIP	62	19/SEP/08A	16/NOV/08	420	420	56							
D00995	APP GL1-Permanent Works Intake AIP	92	17/NOV/08	16/FEB/09	420	420	0							
D01006	P&S GL1-Temp Works & Drainage Diversion AIP	62	18/SEP/08A	16/NOV/08	395	395	56							
D01007	APP GL1-Temp Works & Drainage Diversion AIP	92	17/NOV/08	16/FEB/09	395	395	0							
<b>Section 25 (Portion CR1)</b>														
D01950	P&S CR1-Permanent Works Intake AIP	63	01/DEC/08*	01/FEB/09	462	462	0							
D01966	P&S CR1-Temp Works & Drainage Diversion AIP	63	01/DEC/08*	01/FEB/09	402	402	0							
<b>Section 13 (Portion BR5)</b>														
D01300	P&S BR5-Permanent Works Intake AIP	62	16/NOV/08*	16/JAN/09	484	484	0							
D01305	APP BR5-Permanent Works Intake AIP	92	17/JAN/09	18/APR/09	484	484	0							
D01316	P&S BR5-Temp Works & Drainage Diversion AIP	62	16/NOV/08*	16/JAN/09	422	422	0							
D01317	APP BR5-Temp Works & Drainage Diversion AIP	92	17/JAN/09	18/APR/09	422	422	0							
<b>Section 11 (Portion BR4)</b>														
D01190	P&S BR4-Permanent Works Intake AIP	62	16/OCT/08A	16/DEC/08	575	575	8							
D01195	APP BR4-Permanent Works Intake AIP	92	17/DEC/08	18/MAR/09	575	575	0							
D01206	P&S BR4-Temp Works & Drainage Diversion AIP	62	18/OCT/08A	18/DEC/08	599	597	4							
D01207	APP BR4-Temp Works & Drainage Diversion AIP	92	19/DEC/08	20/MAR/09	599	597	0							
D01208	P&S BR4-Temp Works & Drainage Diversion DDA	62	01/JAN/09*	03/MAR/09	522	522	0							
D01230	P&S BR4-Permanent Slopeworks AIP	62	21/OCT/08*	21/DEC/08	985	1,065	0							
D01235	APP BR4-Permanent Slopeworks AIP	122	22/DEC/08	22/APR/09	985	1,065	0							
D01240	P&S BR4-Permanent Slopeworks DDA	62	16/JAN/09*	18/MAR/09	477	477	0							
<b>Section 16 (Portion B2)</b>														
D01450	P&S B2-Permanent Works Intake AIP	62	16/NOV/08*	16/JAN/09	524	524	0							
D01455	APP B2-Permanent Works Intake AIP	92	17/JAN/09	18/APR/09	524	524	0							
D01466	P&S B2-Temp Works & Drainage Diversion AIP	62	16/NOV/08*	16/JAN/09	477	477	0							
D01467	APP B2-Temp Works & Drainage Diversion AIP	92	17/JAN/09	18/APR/09	477	477	0							
<b>Adits &amp; Stilling Chambers</b>														
D00520	P&S Adits & Stilling Chamber Temp Support AIP	79	16/JUL/08A	27/OCT/08	116	91	90							
D00525	APP Adits & Stilling Chamber Temp Support AIP	92	28/OCT/08	27/JAN/09	116	91	0							
D00540	P&S Adits & SC Permanent Lining AIP	33	21/OCT/08*	22/NOV/08	97	91	0							
D00545	APP Adits Permanent Lining AIP	92	23/NOV/08	22/FEB/09	97	91	0							
D00560	P&S SCs Permanent Lining AIP	33	30/OCT/08*	01/DEC/08	82	82	0							
D00565	APP SCs Permanent Lining AIP	92	02/DEC/08	03/MAR/09	82	82	0							
<b>Project Wide</b>														
D00145	APP Detailed Const Risk Assess(Portals) DDA	42	02/AUG/08A	27/OCT/08	11	12	80							
D00147	P&S Det Const Risk Assess Vol 1-(W0) DDA	24	09/SEP/08A	29/OCT/08	0	8	60							
D00148	APP Det Const Risk Assess Vol 1-(W0) DDA	60	30/OCT/08	28/DEC/08	0	8	0							
D00149	P&S DCRA V2-PFLR1,SM1,HKU1,E7,MBD2,MB16,etc DDA	63	30/OCT/08*	31/DEC/08	86	86	0							
D00150	APP DCRA V2-PFLR1,SM1,HKU1,E7,MBD2,MB16,etc DDA	92	01/JAN/09	02/APR/09	86	86	0							
D00160	P&S Impact Assess Rep Waterwork Fac V 1-(W0) DDA	24	24/SEP/08A	27/OCT/08	0	-11	90							
D00161	APP Impact Assess Rep Waterwork Fac V 1-(W0) DDA	40	28/OCT/08	06/DEC/08	0	-11	0							
D00162	P&S Impact ARW V 2-PFLR1,SM1,HKU1,THR2,etc DDA	63	21/NOV/08*	22/JAN/09	183	183	0							
D00168	P&S Water Inflow Assess Rep(Tunnel, Adit & DS)	61	30/OCT/08*	29/DEC/08	24	24	0							
D00169	APP Water Inflow Assess Rep(Tunnel, Adit & DS)	60	30/DEC/08	27/FEB/09	24	24	0							
D00188	P&S Blasting Assessment - Volume 2B(Adit W0)	50	30/APR/08A	16/OCT/08A	0		100							
D00189	APP Blasting Assessment - Volume 2B(Adit W0)	92	17/OCT/08A	17/JAN/09	0	1,160	3							
D00190	P&S BA - Vol 3A(E5A,MB16,MBD2,E7,THR2,HR1,GL1)	93	21/OCT/08*	21/JAN/09	177	157	0							
D00192	P&S BA-Vol 3B MA17,M3,TP789,TP4-5,HKU1,PFLR1,SM1	93	01/DEC/08*	03/MAR/09	113	113	0							
<b>Main Tunnel</b>														
D00440	P&S Adit/main tun intrct Temp Sup(excl W0) AIP	51	15/AUG/08A	27/OCT/08	269	246	90							
D00445	APP Adit/main tun intrct Temp Sup(excl W0) AIP	122	28/OCT/08	26/FEB/09	269	246	0							
D00500	P&S TBM Dismantle Chamber Temp Supt at W0 AIP	194	16/MAY/08A	30/NOV/08	672	672	78							
D00505	APP TBM Dismantle Chamber Temp Supt at W0 AIP	92	01/DEC/08	02/MAR/09	672	672	0							
D00510	P&S TBM Dismantle Chamber Temp Supt at W0 DDA	63	30/DEC/08*	02/MAR/09	671	671	0							
<b>Milestone</b>														
<b>Design Submission</b>														
M2-1070	2.07-AIP-Adits&Stilling Chambers Submission	0		03/OCT/08A	1,137		100							
M2-1110	2.11-AIP-Dropshaft Submission	0		15/DEC/08	1,108	1,193	0							
M2-1151	2.15A - AIP-Intakes Submission (33%)	0		01/SEP/08A	0		100							
M2-1190	2.19-AIP Slope Protective(other thanE&W Portals)	0		01/JAN/09	1,091	1,176	0							

Start Date 23/NOV/07  
 Finish Date 22/MAR/12  
 Data Date 21/OCT/08  
 Run Date 25/OCT/08 14:52


810A

Design & Construction of Hong Kong  
 West Drainage Tunnel  
 Contract No. DC/2007/10  
 Works Programme  
 3 Monthly Rolling Programme  
 OCT MONTHLY REPORT

Sheet 3 of 6


Dragages - Nishimatsu Joint Venture 寶嘉 - 西松建設

Date	Revision	Checked	Approved
25/OCT/08	11th Monthly Update		
23/Sep08	21/Oct08		

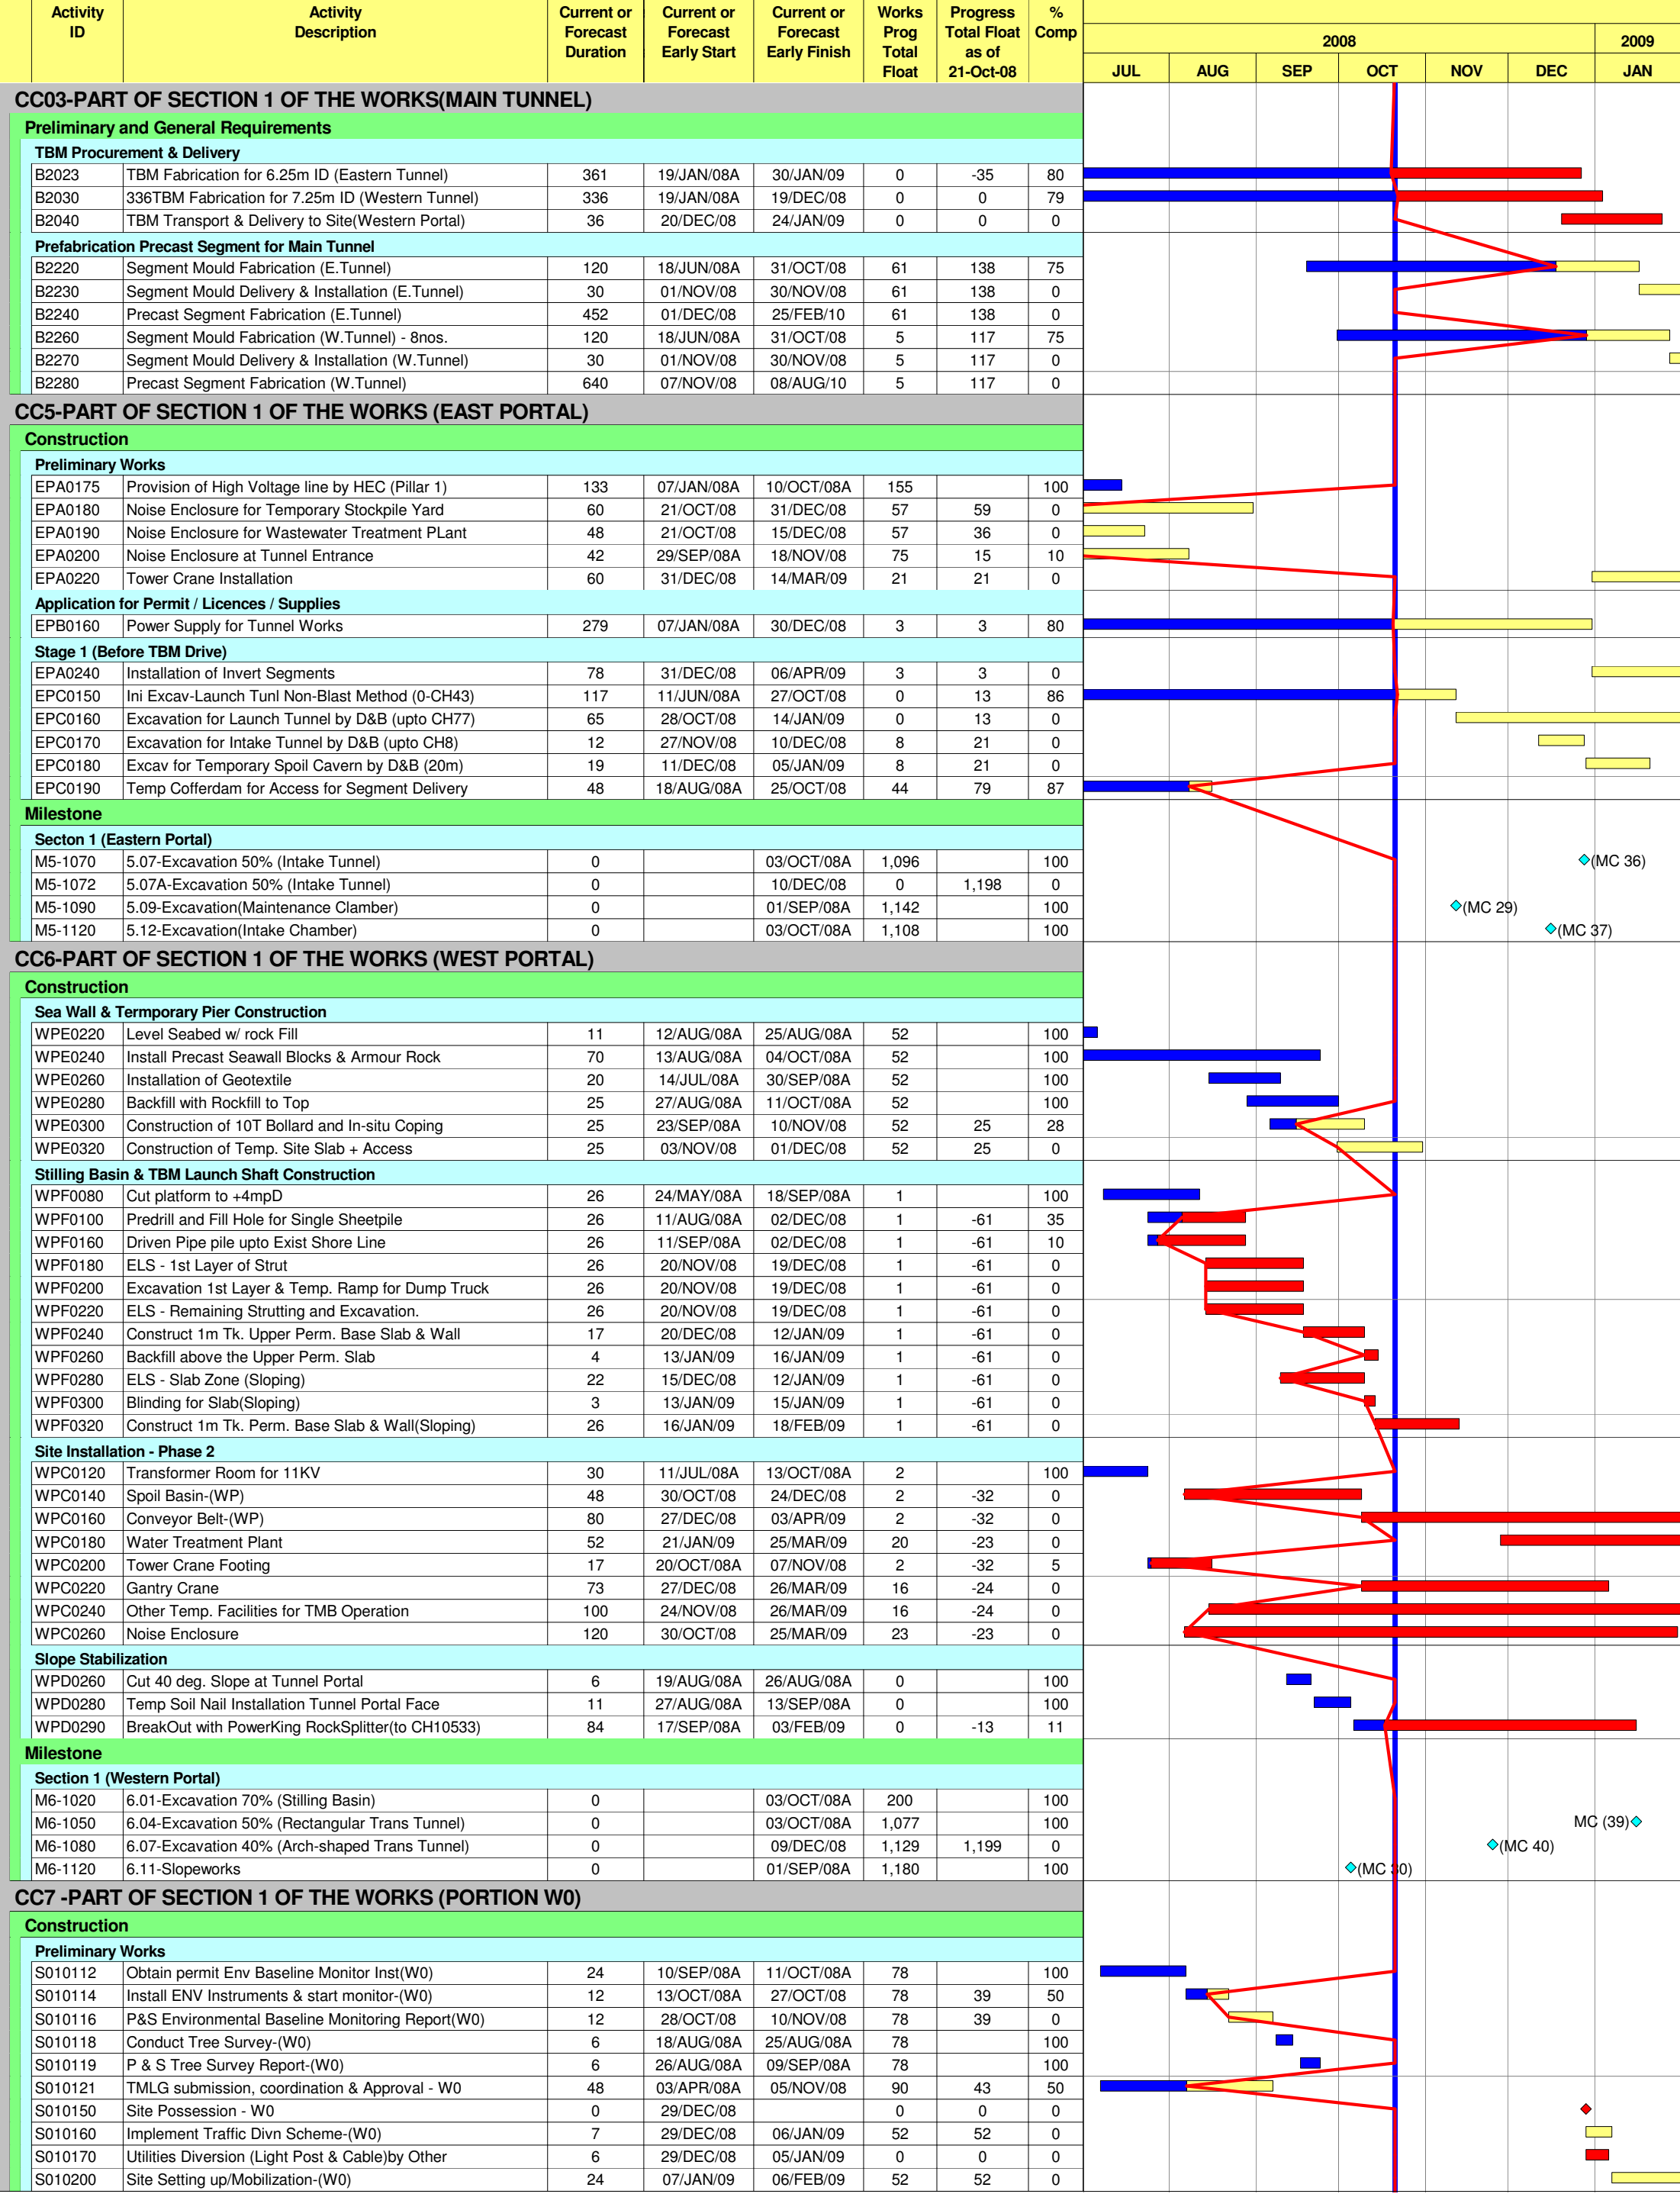

Activity ID	Activity Description	Current or Forecast Duration	Current or Forecast Early Start	Current or Forecast Early Finish	Works Prog Total Float	Progress Total Float as of 21-Oct-08	% Comp	2008						2009
								JUL	AUG	SEP	OCT	NOV	DEC	JAN
<b>Preparation Works</b>														
S010180	Install Geotech Monitoring Instruments-(W0)	6	29/DEC/08	05/JAN/09	0	0	0							
S010220	Pre-drilling & Grouting Works-(W0)	24	14/JAN/09	13/FEB/09	60	60	0							
<b>Intakes - External Structures (Stage1)</b>														
S010190	Cofferdam Wall Driving-(W0)	65	06/JAN/09	25/MAR/09	0	0	0							
<b>CC8 - SECTION 2 OF THE WORKS (PORTION E5A)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S020020	Conduct Ground Investigation Works - E5A	27	08/SEP/08A	04/OCT/08A	116		100							
S020025	Conduct Utility Identification Works - E5A	43	03/SEP/08A	18/OCT/08A	116		100							
S020030	Prepare Utility Diversion Plans - E5A	70	21/OCT/08	13/JAN/09	116	95	0							
S020040	Notify,Coord&Obtain Permit-Utility Prov - E5A	149	14/JAN/09	28/JUL/09	116	95	0							
<b>CC9 - SECTION 3 OF THE WORKS (PORTION E5B)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S030010	Prepare Utility Diversion Plans - E5B	70	21/OCT/08	13/JAN/09	209	122	0							
S030020	Notify,Coord&Obtain Permit-Utility Prov - E5B	149	14/JAN/09	28/JUL/09	209	122	0							
<b>CC10-SECTION 4 OF THE WORKS (PORTION MB16)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S040010	Conduct Ground Investigation Works - MB16	44	18/JUL/08A	24/SEP/08A	28		100							
S040020	Prepare Utility Diversion Plans - MB16	70	21/OCT/08	13/JAN/09	28	-25	0							
S040030	Notify,Coord&Obtain Permit-Utility Prov - MB16	149	14/JAN/09	28/JUL/09	28	-25	0							
S040100	Notify SO for Portion Possession - (MB16)	0		02/JAN/09*	0	0	0							
S040110	25 wks prior to Portion Possess Date-(MB16)	175	03/JAN/09	26/JUN/09	0	0	0							
S040112	Obtain permit Inst Env Base Monitor Inst(MB16)	24	03/JAN/09	03/FEB/09	73	73	0							
S040121	TMLG submission, coordination & Approval - MB16	48	03/JAN/09	03/MAR/09	85	85	0							
<b>CC11-SECTION 5 OF THE WORKS (PORTION MBD2)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S050010	Conduct Ground Investigation Works - MBD2	30	14/AUG/08A	13/SEP/08A	91		100							
S050015	Conduct Utility Identification Works - MBD2	40	08/SEP/08A	28/OCT/08	81	70	82							
S050020	Prepare Utility Diversion Plans - MBD2	70	29/OCT/08	21/JAN/09	81	70	0							
<b>CC12-SECTION 6 OF THE WORKS (PORTION E7)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S060020	Prepare Utility Diversion Plans - E7	70	21/OCT/08	13/JAN/09	76	20	0							
S060030	Notify,Coord&Obtain Permit-Utility Prov - E7	149	14/JAN/09	28/JUL/09	76	20	0							
<b>CC13-SECTION 7 OF THE WORKS (PORTION THR2)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S070010	Prepare Utility Diversion Plans - THR2	70	21/OCT/08*	13/JAN/09	52	-35	0							
S070020	Notify,Coord&Obtain Permit-Utility Prov - THR2	149	14/JAN/09	28/JUL/09	52	-35	0							
S070100	Notify SO for Portion Possession - (THR2)	0		19/DEC/08*	0	0	0							
S070110	25 wks prior to Portion Possess Date-(THR2)	175	20/DEC/08	12/JUN/09	0	0	0							
S070112	Obtain permit Env Base Monitor Inst(THR2)	24	20/DEC/08	20/JAN/09	72	72	0							
S070114	Install ENV Instruments & start monitor(THR2)	12	21/JAN/09	06/FEB/09	72	72	0							
<b>CC14-SECTION 8 OF THE WORKS (PORTION GL1)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S080010	Conduct Ground Investigation Works - GL1	0	25/SEP/08A	04/OCT/08A	222		100							
S080015	Conduct Utility Identification Works - GL1	45	18/SEP/08A	04/OCT/08A	217		100							
S080020	Prepare Utility Diversion Plans - GL1	70	21/OCT/08	13/JAN/09	217	250	0							
S080030	Notify,Coord&Obtain Permit-Utility Prov - GL1	149	14/JAN/09	28/JUL/09	217	250	0							
<b>CC15-SECTION 9 OF THE WORKS (PORTION HR1)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S090020	Prepare Utility Diversion Plans - HR1	70	21/OCT/08*	13/JAN/09	329	242	0							
S090030	Notify,Coord&Obtain Permit-Utility Prov - HR1	149	14/JAN/09	28/JUL/09	329	242	0							
<b>CC16-SECTION 10 OF THE WORKS (PORTION DG1)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S100020	Prepare Utility Diversion Plans - DG1	70	21/OCT/08	13/JAN/09	234	193	0							
S100030	Notify,Coord&Obtain Permit-Utility Prov - DG1	149	14/JAN/09	28/JUL/09	234	193	0							
<b>CC20-SECTION 14 OF THE WORKS (PORTION BR6)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S140010	Conduct Ground Investigation Works - BR6	29	18/AUG/08A	17/SEP/08A	251		100							
S140015	Conduct Utility Identification Works - BR6	39	05/AUG/08A	05/SEP/08A	251		100							
S140020	Prepare Utility Diversion Plans - BR6	70	21/OCT/08	13/JAN/09	251	227	0							
S140030	Notify,Coord&Obtain Permit-Utility Prov - BR6	149	14/JAN/09	28/JUL/09	251	227	0							
<b>Milestone</b>														
<b>Section 14 (Portion BR6)</b>														
M201010	20.01-Pre-drilling & Grouting Works (Dropshaft)	0		01/SEP/08A	481		100							
<b>CC21-SECTION 15 OF THE WORKS (PORTION W3)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S150010	Conduct Ground Investigation Works - W3	23	16/SEP/08A	17/OCT/08A	77		100							
S150015	Conduct Utility Identification Works - W3	39	16/SEP/08A	20/SEP/08A	222		100							
S150020	Prepare Utility Diversion Plans - W3	70	21/OCT/08	13/JAN/09	222	212	0							
S150030	Notify,Coord&Obtain Permit-Utility Prov - W3	149	14/JAN/09	28/JUL/09	222	212	0							
<b>CC25-SECTION 19 OF THE WORKS (PORTION MA17)</b>														
<b>Construction</b>														
<b>Preliminary Works</b>														
S190010	Conduct Ground Investigation Works - MA17	54	21/OCT/08	22/DEC/08	159	105	0							
S190015	Conduct Utility Identification Works - MA17	73	25/AUG/08A	18/OCT/08A	140		100							
S190020	Prepare Utility Diversion Plans - MA17	70	23/DEC/08	20/MAR/09	140	105	0							

Start Date 23/NOV/07  
 Finish Date 22/MAR/12  
 Data Date 21/OCT/08  
 Run Date 25/OCT/08 14:52



810A

Sheet 5 of 6


Design & Construction of Hong Kong West Drainage Tunnel  
 Contract No. DC/2007/10  
 Works Programme  
 3 Monthly Rolling Programme  
 OCT MONTHLY REPORT



Date	Revision	Checked	Approved
25/OCT/08	11th Monthly Update		
23/Sep/08	21/Oct/08		

Activity ID	Activity Description	Current or Forecast Duration	Current or Forecast Early Start	Current or Forecast Early Finish	Works Prog Total Float	Progress Total Float as of 21-Oct-08	% Comp	2008							2009
								JUL	AUG	SEP	OCT	NOV	DEC	JAN	
<b>CC26-SECTION 20 OF THE WORKS (PORTION M3)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S200010	Conduct G Investigation Works - M3	48	18/AUG/08A	26/SEP/08A	199		100								
S200020	Prepare Utility Diversion Plans - M3	70	21/OCT/08	13/JAN/09	199	150	0								
S200030	Notify,Coord&Obtain Permit-Utility Prov - M3	149	14/JAN/09	28/JUL/09	199	150	0								
<b>CC27-SECTION 21 OF THE WORKS (PORTION TP789)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S210010	Conduct Ground Investigation Works -TP789	63	18/AUG/08A	13/SEP/08A	98		100								
S210020	Prepare Utility Diversion Plans - TP789	70	21/OCT/08	13/JAN/09	98	92	0								
S210030	Notify,Coord&Obtain Permit-Utility Prov - TP789	149	14/JAN/09	28/JUL/09	98	92	0								
<b>CC28-SECTION 22 OF THE WORKS (PORTION TP5)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S220010	Conduct Ground Investigation Works -TP5	37	14/OCT/08A	25/NOV/08	66	57	16								
S220015	Conduct Utility Identification Works - TP5	44	21/OCT/08	10/DEC/08	59	44	0								
S220020	Prepare Utility Diversion Plans - TP5	70	11/DEC/08	09/MAR/09	59	44	0								
<b>CC29-SECTION 23 OF THE WORKS (PORTION TP4)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S230010	Conduct Ground Investigation Works -TP4	47	18/SEP/08A	14/NOV/08	86	44	53								
S230020	Prepare Utility Diversion Plans - TP4	70	15/NOV/08	11/FEB/09	86	44	0								
<b>CC30-SECTION 24 OF THE WORKS (PORTION W5)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S240010	Conduct Ground Investigation Works -W5	29	20/SEP/08A	04/OCT/08A	100		100								
S240015	Conduct Utility Identification Works - W5	43	13/OCT/08A	01/DEC/08	86	72	16								
S240020	Prepare Utility Diversion Plans - W5	70	02/DEC/08	27/FEB/09	86	72	0								
<b>CC31-SECTION 25 OF THE WORKS (PORTION CR1)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S250015	Conduct Utility Identification Works - CR1	45	10/OCT/08A	26/NOV/08	228	228	20								
S250020	Prepare Utility Diversion Plans - CR1	70	27/NOV/08	23/FEB/09	228	228	0								
<b>CC32-SECTION 26 OF THE WORKS (PORTION RR1)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S260010	Conduct Ground Investigation Works -RR1	37	21/OCT/08	02/DEC/08	35	28	0								
S260015	Conduct Utility Identification Works - RR1	45	13/OCT/08A	03/DEC/08	32	27	15								
S260020	Prepare Utility Diversion Plans - RR1	70	04/DEC/08	02/MAR/09	32	27	0								
<b>CC33-SECTION 27 OF THE WORKS (PORTION W8)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S270010	Conduct Ground Investigation Works -W8	20	21/OCT/08	12/NOV/08	138	111	0								
S270015	Conduct Utility Identification Works - W8	44	08/OCT/08A	18/OCT/08A	114		100								
S270020	Prepare Utility Diversion Plans - W8	70	13/NOV/08	09/FEB/09	114	111	0								
<b>CC34-SECTION 28 OF THE WORKS (PORTION P5)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S280010	Conduct Ground Investigation Works -P5	36	08/SEP/08A	17/OCT/08A	87		100								
S280015	Conduct Utility Identification Works - P5	91	08/SEP/08A	14/NOV/08	93	80	75								
S280020	Prepare Utility Diversion Plans - P5	70	15/NOV/08	11/FEB/09	87	80	0								
<b>CC35-SECTION 29 OF THE WORKS (PORTION W10)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S290010	Conduct GI & Utility Identification Works - W10	24	08/AUG/08A	20/OCT/08A	175		100								
S290015	Conduct Utility Identification Works - W10	41	12/AUG/08A	06/SEP/08A	158		100								
S290020	Prepare Utility Diversion Plans - W10	70	21/OCT/08	13/JAN/09	158	102	0								
S290030	Notify,Coord&Obtain Permit-Utility Prov - W10	100	14/JAN/09	25/MAY/09	158	102	0								
<b>CC36-SECTION 30 OF THE WORKS (PORTION HKU1)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S300010	Prepare Utility Diversion Plans - HKU1	70	21/OCT/08*	13/JAN/09	101	15	0								
S300020	Notify,Coord&Obtain Permit-Utility Prov - HKU1	149	14/JAN/09	28/JUL/09	101	15	0								
<b>CC37-SECTION 31 OF THE WORKS (PORTION PFLR1)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S310905	Prepare Utility Diversion Plans - PFLR1	70	21/OCT/08*	13/JAN/09	74	-12	0								
S310915	Notify,Coord&Obtain Permit-Utility Prov - PFLR1	149	14/JAN/09	28/JUL/09	74	-12	0								
S310920	Notify SO for Portion Possession - (PFLR1)	0		20/JAN/09*	0	0	0								
S310930	25 wks prior to Portion Possess Date-(PFLR1)	175	21/JAN/09	14/JUL/09	0	0	0								
S310932	Obtain permit Env Base Monitor Inst(PFLR1)	24	21/JAN/09	20/FEB/09	71	71	0								
<b>CC38-SECTION 32 OF THE WORKS (PORTION SM1)</b>															
<b>Construction</b>															
<b>Preliminary Works</b>															
S320905	Prepare Utility Diversion Plans - SM1	70	21/OCT/08*	13/JAN/09	39	-47	0								
S320915	Notify,Coord&Obtain Permit-Utility Prov - SM1	149	14/JAN/09	28/JUL/09	39	-47	0								
S320920	Notify SO for Portion Possession - SM1)	0		04/DEC/08*	0	0	0								
S320930	25 wks prior to Portion Possess Date-(SM1)	175	05/DEC/08	28/MAY/09	0	0	0								
S320932	Obtain permit Install Env Base Monitor Inst(SM1)	24	05/DEC/08	05/JAN/09	73	73	0								
S320934	Install ENV Instruments & start monitor(SM1)	12	06/JAN/09	19/JAN/09	73	73	0								
S320936	P & S Environmental Base Monitoring Report(SM1)	12	20/JAN/09	05/FEB/09	73	73	0								
B2026	TBM Transport & Delivery to Site(Eastern Portal)	38	31/JAN/09	09/MAR/09	0	-35	0								

Start Date 23/NOV/07  
 Finish Date 22/MAR/12  
 Data Date 21/OCT/08  
 Run Date 25/OCT/08 14:52



Date	Revision	Checked	Approved
25/OCT/08	11th Monthly Update		
	23Sep08 - 21Oct08		

---

---

**APPENDIX P**  
**WASTE GENERATED QUANTITY**

---

---

## Monthly Waste Flow Table

Quarter ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete (see Note 3)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see notes 2)	Chemical Waste	Others, e.g. general refuse
	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )	( in ' 000 m <sup>3</sup> )
Feb-08											40 m <sup>3</sup>
Mar-08					6 m <sup>3</sup>						84 m <sup>3</sup>
Apr-08					34 m <sup>3</sup>						34 m <sup>3</sup>
May-08					566 m <sup>3</sup>			2 m <sup>3</sup>			39 m <sup>3</sup>
Jun-08					486 m <sup>3</sup>	30 m <sup>3</sup>				0.4 m <sup>3</sup>	6 m <sup>3</sup>
Jul-08					1311 m <sup>3</sup>	3004 m <sup>3</sup>				0.2 m <sup>3</sup>	45 m <sup>3</sup>
Aug-08			1100 m <sup>3</sup>		904 m <sup>3</sup>	2404 m <sup>3</sup>		2 m <sup>3</sup>		0.2 m <sup>3</sup>	34 m <sup>3</sup>
Sep-08			1620 m <sup>3</sup>		64 m <sup>3</sup>	11504 m <sup>3</sup>					11 m <sup>3</sup>
Oct-08			650 m <sup>3</sup>		2488 m <sup>3</sup>	1882 m <sup>3</sup>					28 m <sup>3</sup>
Nov-08											
Dec-08											
<b>Total</b>	<b>0</b>	<b>0</b>	<b>3370 m<sup>3</sup></b>	<b>0</b>	<b>5859 m<sup>3</sup></b>	<b>18824 m<sup>3</sup></b>	<b>0</b>	<b>4 m<sup>3</sup></b>	<b>0</b>	<b>0.8 m<sup>3</sup></b>	<b>321 m<sup>3</sup></b>

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (2) Plastics refer to plastic bottles/containers, plastic/foam from packaging material.
  - (3) Broken concrete for recycling into aggregates.
  - (4) The Figures for October 2008 are as of 31-10-08.
