

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

**Contract No. EP/SP/58/08**  
**Sludge Treatment Facilities**  
**Environmental Monitoring and Audit Report**  
**For**  
**August 2011**

MaterialLab Ref No.: 100440EN111343

Certified by :



John K. M. Ho  
(Environmental Team Leader)

Date :

04 September 2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division



Fugro Development Centre,  
5 Lok Yi Street,  
17 M.S. Castle Peak Road, Tai Lam,  
Tuen Mun, N.T., Hong Kong.  
Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

Date 10 September 2011  
Our Ref. MTL/CH/1500/2011/C

Veolia Water - Leighton – John Holland Joint Venture  
30/F Tower 1 Kowloon Commerce Centre,  
No. 51 Kwai Cheong Road,  
Kwai Chung, Hong Kong.

**Attn. : Mr. Andrew Watson**

**By fax & mail**  
Fax : 2430 8022

Dear Sir,

**Contract No. EP/SP/53/08 -  
Sludge Treatment Facilities  
Monthly Monitoring Report for August 2011**

We enclose herewith one original, seven copies and two electric copies of the Monthly Monitoring Report for August 2011 (100440EN111343) for the captioned project.

Should there be any queries, please feel free to contact us.

Assuring you of our best services at all times.

Yours faithfully,  
for and on behalf of  
FUGRO TECHNICAL SERVICES LIMITED

John Ho  
Environmental Team Leader  
Chemical & Environmental

JH/kc

9 September 2011  
Our Ref: 8764/0193

By Post

VW-VES (HK) Limited  
Level 30, Tower 1  
Kowloon Commercial Centre,  
No. 51 Kwai Cheong Road,  
Kwai Chung,  
Hong Kong

Attention: Mr. Vincent Deleu, Project Manager

Dear Sir,

**CONTRACT NO. EP/SP/58/08 DESIGN, BUILD AND OPERATE OF SLUDGE  
TREATMENT FACILITIES  
- MONTHLY ENVIRONMENTAL MONITORING AND AUDIT REPORT (AUGUST 2011)**

I refer to the revised report from Environmental Team provided on 8 September 2011. I do not have further comment and have verified the captioned report.

Yours faithfully  
**BMT Asia Pacific Limited**



Claudine Lee  
Independent Environmental Checker

Cc. Environmental Manager – Mr. Chris Chan (By email)  
ET Leader - Fugro Technical Services Ltd., Mr. John Ho (By email)

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

---

### CONTENTS

1. Executive Summary
2. Introduction
3. General Review
4. Construction Phase Environmental Monitoring
5. Construction Site Environmental Audit
6. Summary of Complaints, Summons and Successful Prosecutions
7. Works Programme for September 2011
8. Monitoring Schedule for September 2011
9. Comments and Conclusions for the reporting period

#### *Appendices:*

- Appendix 1: Water Quality Monitoring Location
- Appendix 2: Equipment Calibration Certificates
- Appendix 3: Stream and Marine Water Quality Monitoring Data
- Appendix 4: Graphical Presentation of Monitoring Data
- Appendix 5: Construction Program
- Appendix 6: Management Structure and Organization Chart
- Appendix 7: Event / Action Plan for Water Quality
- Appendix 8: Implementation Schedule of Mitigation Measures
- Appendix 9: Incident Report on Action Level or Limit Level Non-compliance

#### *List of Tables:*

- Table 3.1 The Contact Persons and Telephone Numbers of Key Personnel
- Table 3.2 Summary of Monitored Parameters
- Table 3.3 Action and Limit Levels for Marine and Stream Water Quality
- Table 3.4 Action Level for Landfill Gas Measurement
- Table 4.1 Method Statements of Laboratory Analysis of Marine Water Quality
- Table 4.2 Method Statements of Laboratory Analysis of Stream Water Quality
- Table 4.3 Water Quality Monitoring Equipment
- Table 4.4. Monitoring Schedule from 25 July to 24 August 2011
- Table 4.5 Water Quality Monitoring Results
- Table 4.6 Summary of Exceedances from 25 July to 24 August 2011
- Table 4.7 Landfill Gas Monitoring Equipment
- Table 4.8 Ecological Survey Checklist for August 2011

---

**FUGRO TECHNICAL SERVICES LIMITED**

Materialab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk

---

**Materialab**

- Table 4.9 Record of Implementation of the Proposed Landscape and Visual Mitigation Measures in Construction Phase
- Table 4.10 Photographic Record of Landscape and Visual Impact Survey
- Table 5.1 Waste Flow Summary
- Table 8.1 Monitoring Schedule for September 2011

*List of Figures:*

- Figure 1.1 Construction Works Area
- Figure 3.1 Site Layout Plan
- Figure 3.2 WENT Landfill Gas Control Zone
- Figure 4.1 Ecological Transect Route

## 1. Executive Summary

Construction work commenced on 22 December 2010. It was of main concern to ascertain whether there was any undesirable effect of the construction activities on various environmental parameters over the site area and the surrounding environment. Impact environmental monitoring on water quality, ecology and landscape and visual impact were carried out to acquire data for assessing any impact associated with the construction activities. This report covers the period from 25 July to 24 August 2011 inclusive.

### Marine Water Quality

Pursuant to EM&A manual, marine water quality monitoring is required during the foundation piling. Piling work was commenced on 21 February 2011 while marine water quality monitoring was conducted during the reporting period.

Marine water quality monitoring for 28 July 2011 (p.m.) was cancelled due to adverse weather condition and safety concern.

Full compliance was achieved in this reporting month.

### Stream Water Quality

As far as the water quality was concerned, 20 events of non-compliance of Action / Limit levels on various monitored parameters were recorded in the reporting period.

The recorded exceedances are not caused by the construction activities so there was no action taken with regards to the action plan.

In general, the stream water quality was not significantly deteriorated after the commencement of the major construction works on 21 February 2011.

### Landfill Gas Monitoring

There was no excavation in the WENT Landfill Consultation Zone in the reporting period. Monitoring for landfill gas was not carried out in the reporting period.

### Ecology Monitoring

Four surveys were conducted on 27 July 2011, 4, 11 and 18 August 2011 at the Middle Lagoon. Total of 48 nos. of birds of 8 species was recorded on 11 August 2011. None of the birds showed any apparent signs of disturbance arising from the STF construction activities. All measures were followed to minimize the disturbance of the wildlife. No disturbance was observed while piling work in progress.

### Landscape and Visual Monitoring

Landscape and visual impact monitoring was conducted on 10 and 19 of August 2011. Details are presented in Section 4.4.

---

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

---

**Works Undertaken During Reporting Period**

The construction phase commenced on 22 December 2010, major site activities conducted in the reporting period includes:

- PFA layer compaction in the site area.
- Cut and fill operation at areas for piling
- Piling at North part of the site
- Construction of EPC's office at the North-west corner of the site
- Excavation of sludge bunkers at plant A & B.

Works area is shown in Figure 1.1

**Reporting Changes and Future Key Issues**

It is anticipated that the existing operation should not create significant nuisance and disturbance on the environmental aspects of air quality, noise level and water quality. Foundation piling was started on 21 February 2011 and throughout the reporting period. Contractor should implement proposed measures to minimize potential impact to the noise and prevent releasing of heavy metals into the Deep Bay Water Control Zone.

**Complaints, Summons and Successful Prosecutions**

As far as complaints, summons and successful prosecutions on the construction work in respect of the environmental protection and pollution control was concerned, there was no documented correspondence received in the reporting period.

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

---

**MaterialLab**

### 2. Introduction

This monthly report reviews the progress of the environmental monitoring and audit work at the site for Contract No. EP/SP/58/08 from 25 July 2011 to 24 August 2011 (the reporting period) and forecasts the activities for September 2011. The monitoring results for water quality are presented in Appendix 3 and the corresponding graphical plots are shown in Appendix 4. Since results of all heavy metal content were less than detection limit, no graphical presentation for marine water quality results for the reporting period is included. Findings of Ecology and Landscape monitoring are presented in Section 4.



---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

---

### 3. General Review

#### 3.1 Background

The Contractor, VW-VES (HK) Limited, has been awarded a contract by the Environmental Protection Department of the Government of the Hong Kong Special Administrative Region for the Sludge Treatment Facilities. The location of the site is shown in Figure 3.1.

The program commenced in November 2010 and is anticipated to complete in 2013.

The construction schedule will be based on the major works associated with the project. The major works under this contract include:

##### Incineration Plant

- a) Sludge receiving, storage and feeding system
- b) Fluidized bed incinerators
- c) Waste heat recovery and power generation system
- d) Flue gas treatment system
- e) Ash storage and handling system
- f) Residue storage and handling system
- g) Fluidized bed sand storage and handling system
- h) Reagent reception and storage system
- i) Process control and monitoring system

##### Ancillary and supporting Facilities

- a) Weighbridge
- b) Site security
- c) Administration building
- d) Vehicle washing facilities
- e) Maintenance workshop and utility yard
- f) Drainage system
- g) Sewerage system
- h) Sewage treatment works
- i) Water supply system
- j) Deodorization system

Construction program for the captioned project is enclosed in Appendix 5.

Fugro Technical Services Ltd. – MaterialLab Division (MaterialLab) has been commissioned by the client as the Environmental Team which comprises the monitoring staff and the environmental auditor to undertake the environmental monitoring and audit work for this project. The project management structure and organization chart is shown in Appendix 6.

The contact person and telephone numbers of key personnel for the captioned project are shown in Table 3.1.

**Table 3.1 The Contact Persons and Telephone Numbers of Key Personnel**

Company / Department	Role in the Contract	Contact Person	Telephone Number
VW-VES (HK) Limited	Contractor	Mr. Vincent Deleu	2253 2600
Environmental Protection Department	Employer	Mr. Alex Ng	2872 1800
Environmental Protection Department, EIAO	EIAO Officer	Mr. Thomas To	2835 1103
JACOBS	Employer Representative	Mr. Lesile Swann	2880 9788
Fugro Technical Services Ltd. – MaterialLab Division	Environmental Team	Mr. John Ho	2450 8233
BMT Asia Pacific Ltd.	Independent Environmental Checker	Ms. Claudine Lee	2241 9847

### 3.2 Summary of Environmental Monitoring and Audit (EM&A) Requirements

The EM&A program requires the monitoring of water quality prior to the commencement of and during the construction. A baseline report was prepared in December 2010 for the contract based on monitoring data acquired before the commencement of construction works.

Impact monitoring of water quality is to be undertaken at the designated monitoring stations. The monitored parameters are summarized in Table 3.2.

Action and Limit (AL) levels are established based on the data from the baseline report. Should the monitoring results indicate any non-compliance of AL levels, actions according to the Event / Action Plan in Appendix 7 are to be followed and appropriate environmental mitigation measures as in Appendix 8 are to be implemented to rectify the situation. The implementation status of mitigation measures is also shown in Appendix 8.

Impact ecology and visual survey are to be conducted at the construction area on regular basis. Monitoring parameters are tabulated in Table 3.2.

The Contractors (VW-VES (HK) Limited) is responsible for waste control within the construction site, removal of the waste material produced from the site and to implement any mitigation measures to minimize waste or redress problems arising from the waste from the site. The waste material may include any sewage, waste water or effluent containing sand, cement, silt or any other suspended or dissolved material to flow from the site onto any adjoining land, storm sewer, sanitary water, or any waste matter or refuse to be deposited anywhere within the site or onto any adjoining land.

The Contractor shall also pay attention to the Waste Disposal Ordinance, the Dumping at Sea Ordinance, the Public Health and Municipal Services Ordinance and the Water Pollution Control Ordinance, and carry out the appropriate waste management work. The relevant licence / permit, such as the effluent discharge licence, the chemical waste producer registration, etc. shall be obtained. The

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

Contractor shall refer to the relevant booklets issued by EPD when applying for the licence / permit.

The environmental mitigation measures and status for waste management are summarized in Appendix 8.

**Table 3.2 Summary of Monitored Parameters**

Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Marine water	<ul style="list-style-type: none"> <li>▪ Cadmium</li> <li>▪ Chromium</li> <li>▪ Aluminium</li> </ul>	2 monitoring stations and 1 control station	Three days per week for mid-ebb and mid-flood tides during foundation piling of the STF	Sampling is taken at three water depths, namely, 1m below water surface, mid-depth and 1m above sea bed, except where the water depth be less than 6m, in which case the mid-depth station may be omitted. Shall the water depth be less than 3m, only the mid-depth station will be monitored.
Stream water	<ul style="list-style-type: none"> <li>▪ pH</li> <li>▪ Turbidity</li> <li>▪ Suspended solids</li> <li>▪ Dissolved oxygen</li> </ul>	3 monitoring stations and 2 control stations	Three days per week for mid-ebb and mid-flood tides during site formation and foundation piling of the STF and construction of the access road.	<ul style="list-style-type: none"> <li>▪ Two consecutive measurements of DO concentration, DO saturation, turbidity and pH are taken at mid-depth at each location.</li> <li>▪ Water samples for SS measurement is collected at the same depth at each location.</li> </ul>
Ecology	Site condition and bird monitoring	Whole Middle Lagoon and 20 m from the boundary of the Lagoon	<ul style="list-style-type: none"> <li>▪ Monthly monitoring for avifauna.</li> <li>▪ Habitat monitoring at least twice per month.</li> <li>▪ Monthly vegetation monitoring.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Avifauna and their behavior.</li> <li>▪ All birds seen and heard should be identified and counted.</li> <li>▪ Signs of breeding of birds.</li> <li>▪ Coverage of water and PFA filling activities in Middle Lagoon.</li> </ul>
Landscape and Visual Impact	All measures, including compensatory planting, undertaken by both the Contractor and the specialist Landscape Sub-Contractor	East Lagoon	Biweekly	Ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.

**Table 3.2 (Con't)**

Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Landfill gas	<ul style="list-style-type: none"> <li>▪ Oxygen</li> <li>▪ Methane</li> <li>▪ Carbon dioxide</li> </ul>	Excavation, operation in chamber and confined space within the WENT Landfill Control Zone. (See Figure 3.2)	During the construction and operation	<ul style="list-style-type: none"> <li>▪ Excavation between 300mm to 1m deep:                             <ul style="list-style-type: none"> <li>- Directly after the excavation has been completed.</li> <li>- Periodically whilst the excavation remains open.</li> </ul> </li> <li>▪ Excavation deeper than 1m:                             <ul style="list-style-type: none"> <li>- At ground surface before excavations commences.</li> <li>- Immediately before any worker enters the excavation.</li> <li>- At the beginning of each working day for the entire period the excavation remains open.</li> <li>- Periodically whilst the excavation remains open.</li> </ul> </li> </ul>

### 3.3 Action and Limit Levels

#### **Water Quality Limit**

Environmental auditing on the monitoring data is to be undertaken based on the Action and Limit (AL) levels for water quality to check against any non-compliances.

The AL levels for monitored parameters are formulated from the baseline monitoring data. The AL levels for marine and stream water quality are tabulated in Table 3.3.

**Table 3.3 Action and Limit Levels for Marine and Stream Water Quality**

Parameters	Action Level	Limit Level
DO in mg/L (mid-depth)	≤ 5.16	≤ 4
SS in mg/L (mid-depth)	≥ 41 <u>AND</u> 120% of control station's SS on the same day of measurement	≥ 85 <u>AND</u> 130% of control station's SS on the same day of measurement
Turbidity in NTU (mid-depth)	≥ 36.4 <u>AND</u> 120% of control station's turbidity on the same day of measurement	≥ 78.9 <u>AND</u> 130% of control station's turbidity on the same day of measurement
pH	pH ≤ 7.55 or pH ≥ 8.11	pH ≤ 6 or pH ≥ 9

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 3.3 (Con't)**

Parameters	Action Level	Limit Level
Cadmium in µg/L	≥ 0.5	≥ 0.5
Chromium in µg/L	≥ 1	≥ 1
Aluminium in µg/L	≥ 20	≥ 20

**Notes:**

- For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

**Landfill Gas Limit**

Depending on the results of the measurements, actions required will be vary and should be set down by the Safety Officer or other appropriately qualified person. The actions shown in Table 3.4 should be referred as the minimum requirements to be encompassed.

**Table 3.4 Action Level for Landfill Gas Measurement**

Parameter	Measurement	Action
Oxygen	<19 %	<ul style="list-style-type: none"> <li>▪ Ventilate to restore oxygen to &gt;19 %</li> <li>▪ Stop works</li> <li>▪ Evacuate personnel / prohibit entry</li> <li>▪ Increase ventilation to restore oxygen to &gt;19 %</li> </ul>
	<18 %	
Methane	>10 % LEL (i.e. >0.5 % by volume)	<ul style="list-style-type: none"> <li>▪ Prohibit hot works</li> <li>▪ Ventilate to restore methane to &lt;10 % LEL</li> </ul>
	>20 % LEL (i.e. >1 % by volume)	
Carbon dioxide	>0.5 %	<ul style="list-style-type: none"> <li>▪ Ventilate to restore carbon dioxide to &lt;0.5 %</li> <li>▪ Stop works</li> <li>▪ Evacuate personnel / prohibit entry</li> <li>▪ Increase ventilation to restore carbon dioxide to &lt;0.5 %</li> </ul>
	>1.5 %	

#### 4. Construction Phase Environmental Monitoring

The construction phase was commenced on 22 December 2010. During the construction phase, impact water quality monitoring for marine and stream is required. The monitoring locations are shown in Appendix 1.

##### 4.1 Water Quality Monitoring

###### 4.1.1 Monitoring Methodology

###### Marine Water Quality

During the course of foundation piling of the STF, the impact conditions of marine water quality are measured at two monitoring stations and one control station with coordinates as shown in Appendix 1. The Environmental Team Leader shall agree with the IEC and EPD on all the monitoring stations.

During the course of foundation piling, impact monitoring shall be undertaken three days per week, at mid-flood and mid-ebb tides, with sampling and measurement at the designated monitoring stations.

Samples are to be taken at three water depths, namely 1m below water surface, mid-water and 1m above seabed at both mid-flood and mid-ebb tides, except where the water depth is less than 6m, the mid-depth station may be omitted. Should the water depth be less than 3m, only mid-depth will be monitored.

Water samples should be kept in chilled condition (~4°C) during delivery to laboratory and before commencement of the analysis. The parameters of laboratory analysis include Cadmium, Chromium and Aluminium. The method statements are shown in Table 4.1.

Table 4.1 Method Statements of Laboratory Analysis of Marine Water Quality

Parameters	Method	Detection limit, µg/L
Cadmium	USEPA method 6020A	0.5
Chromium		1
Aluminium		20

###### Stream Water Quality

Monitoring of pH, turbidity level (NTU), suspended solids level (mg/L), and dissolved oxygen (mg/L) are conducted at the designated locations including three monitoring stations and two control stations as shown in Appendix 1. The method statements are shown in Table 4.2.

Dissolved oxygen, turbidity and pH are measured *in-situ* while suspended solids content is determined in a HOKLAS accredited laboratory.

Impact monitoring is undertaken three days per week during mid-ebb and mid-flood tides.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 4.2 Method Statements of Laboratory Analysis of Stream Water Quality**

Parameters	Method	Detection limit, mg/L
Suspended solids	APHA, 18 <sup>th</sup> edition, 2540D	1

**4.1.2 Monitoring Equipment**

The equipment employed for the monitoring are presented in Table 4.3 and the calibration certificates are attached in Appendix 2.

**Table 4.3 Water Quality Monitoring Equipment**

Equipment	Model	Parameters Measured
<i>Fieldwork – Marine Water Quality Monitoring</i>		
Global positioning system (GPS)	Trimble Scout Master/Magellan Colotrak	Positioning
Echo sounder	Eagle Magna 3	Depth
Water sampler	Kahlsico 135WB153	Water sampling
<i>Fieldwork – Surface Water Quality Monitoring</i>		
pH meter	Hanna	pH
Dissolved oxygen meter	YSI 58 meter YSI 5739 probe YSI 5795A submersible stirrer	Dissolved oxygen Temperature
Salinity meter	YSI 30 meter/YSI 63 meter	Salinity
Turbidity meter	HACH 2100P	Turbidity
Water sampler	Kahlsico 135WB153/Pitcher	Water sampling
<i>Laboratory Analysis</i>		
Analytical balance	Ohaus AP210S	Suspended solids
Oven	WIB-Binder IP120	Suspended solids
Vacuum pump	GAST DOA-P104-BN	Suspended solids

**4.1.3 Review of the Construction Phase Monitoring Programme**

The schedule for the marine and stream water monitoring programme in the reporting period is shown in Table 4.4.

**Table 4.4 Monitoring Schedule of Stream and Marine Water from 25 July to 24 August 2011**

SUN	MON	TUE	WED	THU	FRI	SAT
	25 July	26 W M	27	28 W M*	29	30 W M
31	1 August	2 W M	3	4 W M	5	6 W M
7	8	9 W M	10	11 W M	12	13 W M
14	15	16 W M	17	18 W M	19	20 W M
21	22	23 W M	24	25	26	27
28	29	30	31			

Legend: W – Stream water quality monitoring at C1, C2, W1, W2 and W3. Three days per week.  
 M – Marine water quality monitoring at DM4, M1 and M2. Three days per week.

\*Marine water quality monitoring for 28 July 2011 (p.m.) was cancelled due to adverse weather condition and safety concern.

#### 4.1.4 Impact Water Quality Monitoring Result

The impact water quality monitoring data, laboratory results and QC data are shown in Appendix 3. The statistical analysis of the data is shown in Table 4.5. Graphical plot of average measurement is enclosed in Appendix 4. Results of all heavy metals content were less than detection limit, no graphical presentation for marine water quality results included.

During the course of the monitoring work, top layer PFA compaction, cut and fill operation, construction of EPC's office, piling works and excavation of sludge bunkers were observed within the project area.

Table 4.5 Water Quality Monitoring Results (25 July to 24 August 2011)

Location	Parameters	Maximum	Minimum	Mean
<i>Stream Water Quality Result</i>				
W1	Dissolved Oxygen (mg/L)	10.39	5.25	6.53
	Turbidity (NTU)	27.60	3.64	12.95
	pH	8.80	7.41	7.79
	Suspended Solids (mg/L)	130.00	3.00	19.44
W2	Dissolved Oxygen (mg/L)	8.93	5.20	6.69
	Turbidity (NTU)	27.50	5.00	14.86
	pH	8.24	7.11	7.66
	Suspended Solids (mg/L)	43.00	7.00	17.40
W3	Dissolved Oxygen (mg/L)	10.62	5.25	7.50
	Turbidity (NTU)	29.30	3.78	11.85
	pH	8.42	7.13	7.75
	Suspended Solids (mg/L)	46.00	5.00	15.37
<i>Marine Water Quality Result</i>				
M1	Cadmium (µg/L)	< 0.5	< 0.5	< 0.5
	Chromium (µg/L)	< 1	< 1	< 1
	Aluminium (µg/L)	< 20	< 20	< 20
M2	Cadmium (µg/L)	< 0.5	< 0.5	< 0.5
	Chromium (µg/L)	< 1	< 1	< 1
	Aluminium (µg/L)	< 20	< 20	< 20

#### 4.1.5 Summary of Non-compliances of the Environmental Quality Performance Limits from 25 July 2011 to 24 August 2011

##### Stream Water Quality

18 events of non-compliance regarding pH and 2 events of non-compliance regarding SS were recorded on various days from 25 July 2011 to 24 August 2011. Details are refers to Appendix 9.



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 4.6 Summary of Exceedances from 25 July to 24 August 2011**

Date & Time	Location	Parameters
26 July 2011, 09:30 to 10:30 (Mid-ebb)	W3	SS: 41 mg/L (Action Level Exceedance) C1 : 3.5 mg/L C2 : 1.5 mg/L
26 July 2011, 10:34 to 11:28 (Mid-ebb)	W1	pH: 8.11 (Action Level Exceedance) C1 : 8.93 C2 : 8.73
26 July 2011, 16:29 to 17:54 (Mid-flood)	W1	pH: 8.8 (Action Level Exceedance) C1 : 9.2 C2 : 8.3
	W2	pH: 8.2 (Action Level Exceedance) C1 : 9.2 C2 : 8.3
	W3	pH: 8.3 (Action Level Exceedance) C1 : 9.2 C2 : 8.3
28 July 2011, 17:40 to 18:02 (Mid-flood)	W1	SS: 125 mg/L (Limit Level Exceedance) C1 : 53 mg/L C2 : 3 mg/L
09 Aug 2011, 09:41 to 11:05 (Mid-ebb)	W1	pH: 7.42 (Action Level Exceedance) C1 : 8.72 C2 : 7.21
	W2	pH : 7.12 (Action Level Exceedance) C1 : 8.72 C2 : 7.21
	W3	pH: 7.14 (Action Level Exceedance) C1 : 8.72 C2 : 7.21
11 Aug 2011, 11:32 to 12:47 (Mid-ebb)	W1	pH: 7.45 (Action Level Exceedance) C1 : 7.15 C2 : 7.08
	W2	pH: 7.24 (Action Level Exceedance) C1 : 7.15 C2 : 7.08
	W3	pH: 7.38 (Action Level Exceedance) C1 : 7.15 C2 : 7.08
11 Aug 2011, 16:55 to 17:57 (Mid-flood)	W2	pH: 7.23 (Action Level Exceedance) C1 : 7.22 C2 : 7.05
	W3	pH: 7.22 (Action Level Exceedance) C1 : 7.22 C2 : 7.05
16 Aug 2011, 08:48 to 10:48 (Mid-flood)	W2	pH: 7.43 (Action Level Exceedance) C1 : 8.26 C2 : 7.49
	W3	pH: 7.51 (Action Level Exceedance) C1 : 8.26 C2 : 7.49

**Table 4.6 (Con't)**

Date & Time	Location	Parameters
23 Aug 2011, 08:40 to 10:23 (Mid-ebb)	W2	pH: 7.23 (Action Level Exceedance) C1 : 8.93 C2 : 7.74
	W3	pH: 8.14 (Action Level Exceedance) C1 : 8.93 C2 : 7.74
23 Aug 2011, 15:15 to 16:31 (Mid-flood)	W1	pH: 8.28 (Action Level Exceedance) C1 : 9.65 C2 : 8.70
	W3	pH: 8.41 (Action Level Exceedance) C1 : 9.65 C2 : 8.70

#### 4.1.6 Review of the Events Non-compliance

##### 4.1.6.1 Marine Water Quality Monitoring

Full compliance was achieved in the reporting period.

##### 4.1.6.2 Stream Water Quality Monitoring

Construction works, include setup of EPC's office, cut and fill operation, piling and excavation of sludge bunkers were in progress throughout the reporting period at the North part of the Lagoon and far away from the Tsang Kok Stream. The stream water quality was at the similar level as that before the piling work. The exceedances were not caused by the construction activities and were subject to the influent of the high or low pH from C1 and/or C2.

18 events of exceedance of pH were recorded at mid-flood or mid-ebb during August at various locations, the events were recorded at W1, W2 and W3 due to influence of low or high pH from upstream of the Tsang Kok stream and not owing to construction activities related.

2 events of exceedance of SS were recorded at mid-flood or mid-ebb of late July at various locations, the events were recorded at W1 and W3 due to occasional collection of dense solid particles at W3 as the low turbidity was taken at W3 during the same sampling period, and stirring up of seabed materials near W1 when the Deep Bay water surface became rough after Typhoon Signal No.1 was hoisted.

The exceedances were unrelated to the construction works, hence the ad-hoc monitoring was cancelled.

The Incident Report on Action and Limit Level Non-compliance is attached in Appendix 9.

## 4.2 Landfill Gas Monitoring

### 4.2.1 Monitoring methodology

4.2.1.1 Routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters into the area.

4.2.1.2 For excavations deeper than 1m measurements should be carried out:

- at the ground surface before excavation commences;
- immediately before any worker enters the excavation;
- at the beginning of each working day for the entire period the excavation remains open; and
- periodically through out the working day whilst workers are in the excavation.

4.2.1.3 For excavations between 300mm and 1m deep, measurements should be carried out:

- directly after the excavation has been completed; and
- periodically whilst the excavation remains open.

4.2.1.4 For excavations less than 300mm and 1m deep, monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person.

4.2.1.5 Depending on the results of the measurements, actions required will vary and should be set down by the Safety Officer or other appropriately qualified person. As a minimum these should encompass those actions specified in Table 3.4.

### 4.2.2 Monitoring equipment

Table 4.7 Landfill Gas Monitoring Equipment

Equipment	Model	Parameters Measured
<i>Fieldwork – Landfill Gas Monitoring</i>		
Landfill Gas Analyzer	RAE QRAE II Multi-gas Detector	Methane, oxygen, carbon dioxide

### 4.2.3 Monitoring result

No excavation or confined space operation in progress inside the WENT Landfill consultation Zone in the reporting period. Monitoring of landfill gas was not required.

## 4.3 Ecological Monitoring

4.3.1 Piling activities commenced on 21 February 2011 and monitoring surveys are to be conducted weekly during these operations. Accordingly, four monitoring visits were conducted on 27 July 2011, 4, 11 and 18 August 2011 to assess the measures in place to minimise the disturbance impact to wildlife. The 3m high hoarding to reduce

disturbance impact of human activities on adjacent areas (namely the Middle Lagoon and other natural habitats) remains in place. No observations of disturbance through construction piling to wildlife on adjacent habitats were made during this and the other monitoring checks conducted during August 2011.

- 4.3.2 Throughout August, no Little Grebes were observed in the rainfall detention ponds within the STF site boundary.
- 4.3.3 Monthly monitoring of avifauna and their notable behaviour, such as breeding activities in the Middle Lagoon, was conducted on 11 August 2011. The Monitoring Area included the whole Middle Lagoon and area extending 20m from the boundary of the Lagoon (see figure 4.1). All birds seen and heard were identified and counted. Any signs of breeding (e.g. nests, recently fledged juveniles) of birds (e.g. Little Grebe) were also recorded. The coverage of water and PFA filling activities in the Middle Lagoon as well as construction activities were also recorded as reference information.
- 4.3.4 The list of bird surveys recorded from the survey conducted on 11 August 2011 can be seen in Table 4.8. Twenty adult Little Grebes and twelve juveniles were recorded in the Middle Lagoon on 11 August; these observations were all recorded approximately 300m or further from the STF site boundary. None of the birds showed any apparent signs of disturbance arising from the STF construction activities. On that date, the coverage of water in the Middle Lagoon was approximately 30%. No PFA filling activities were recorded in the Middle Lagoon.

**Table 4.8 Bird Species observed during Monthly Monitoring Surveys in August 2011**

Survey date: 11 August 2011			
Species Name	Scientific Name	Middle Lagoon	Notable / Breeding Activity
Little Grebe	<i>Tachybaptus ruficollis</i>	32	includes 12 chicks
Little Egret	<i>Egretta garzetta</i>	2	None observed
Common Sandpiper	<i>Actitis hypoleucos</i>	2	None observed
White-throated Kingfisher	<i>Halcyon smyrnensis</i>	1	None observed
White Wagtail	<i>Motacilla alba</i>	1	None observed
Long-tailed Shrike	<i>Lanius schach</i>	3	None observed
Black Drongo	<i>Dicrurus macrocercus</i>	5	None observed
Common Magpie	<i>Pica pica</i>	2	None observed
Total Numbers		48	
Total Species		8	

#### 4.4 Landscape and Visual Impact Monitoring

The landscape and visual impact assessment of the EIA Study recommended a series of mitigation measures to ameliorate the landscape and visual impacts of the Project. The measures for the construction phase as recommended in the EIA Report are summarized in Table 4.9.

Site inspections for the monthly EM&A Record for Landscape and Visual Impact (August 2011) were undertaken on 10 and 19 of August 2011. Observation of the

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

implementation of proposed landscape and visual mitigation measures are summarized in Table 4.9.

**Table 4.9 Record of Implementation of the Proposed Landscape and Visual Mitigation Measures in Construction Phase (August 2011)**

ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status (Aug 2011)	Remarks
CM1	Design / Construction Planning	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Not applicable.	The topsoil was PFA which is not suitable for re-use in the soft landscape works. Suitable topsoil will be imported for planting during landscape planting phase. As confirmed by Leighton, all the PFA has been buried inside the site confinement. PFA attached to the felled trees is washed and retained inside the site boundary.
CM2	Site Practice	Existing trees to be retained on site should be carefully protected during construction.	Tree felling work has commenced since the approval of Phase II tree felling application. Proper procedures of tree felling have been observed during the process. Existing trees to be retained have been carefully protected during construction.	Photographic record of the retained trees are shown in Table 4.10.
CM3	Design / Construction Planning	Trees unavoidably affected by the works should be transplanted where practical.	Tree transplant work has commenced since the approval of Phase II tree felling application. Proper procedures of tree transplant have been observed during the process.	Photographic record of the transplant trees T332 to 359 are shown in Table 4.10.
CM4	Design / Construction Planning	Compensatory tree planting should be provided to compensate for felled trees.	In progress.	Compensatory planting plan has been proposed to and approved by DLO.

**Table 4.9 (Con't)**

ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status (Aug 2011)	Remarks
CM5	Site Practice	Control of night-time lighting.	In progress.	Night time work was implemented from 7pm to 11pm for certain period in Aug 2011. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night time working is shown in Table 4.10.
CM6	Design / Construction Planning	Erection of decorative screen hoarding compatible with the surrounding setting.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.

- CM1** - Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical. Topsoil found within the project site is PFA, which consist of heavy metals and toxic contaminants that it is not suitable to be re-used as soil mix for landscape softwork. Suitable topsoil will be imported for planting during landscape planting phase. All PFA excavated during the tree felling works has been retained in the site confinement. The PFA attached to the felled trees has been washed and retained inside the site boundary.
- CM2** - Existing trees to be retained on site should be carefully protected during construction. The Tree felling work approved under the Phase 1 and 2 tree felling application is about to be completed. Proper procedures of tree felling have been observed. The tree felling works should not cause damages to the existing trees on site. The protective tree fence has been established for the retained trees, and some of the broken branches should be removed to avoid further damages. Photographic records of the retained trees are shown in Table 4.10.
- CM3** - Trees unavoidably affected by the works should be transplanted where practical. Tree transplant works for Tree number T332 to T359 has commenced, and proper tree transplant procedure has been observed according to the method statement. The tree felling work has been completed.
- CM4** - Compensatory tree planting should be provided to compensate for felled trees. Compensatory tree planting has been proposed to and approved by DLO in Phase II tree felling application. The compensatory tree planting has been incorporated with the details of the landscape master plan.
- CM5** - Control of night-time lighting. Night time work was implemented from 7pm to 11pm for certain period in Aug 2011. The lighting is confined to the construction site without affecting the periphery area.
- CM6** - Erection of decorative screen hoarding compatible with the surrounding setting. Construction of decorative screen hoarding compatible with the surrounding setting has been set up in January 2011.

**Table 4.10 Photographic Record of Landscape and Visual Impact Survey**











<p><b>1. Photographic record of the fell trees</b></p>	
	
<p>The tree felling works approved under Phase 1/2 tree felling application have been completed.</p>	<p>The PFA excavated during the tree felling has been carefully washed and retained inside the side boundary.</p>
<p><b>2. Photographic record of protection to the retained trees</b></p>	
	
<p>Proper tree protection fence has been maintained for the retained trees.</p>	<p>Proper tree protection fence has been maintained for the retained trees.</p>
<p><b>3. Photographic record of the transplant trees</b></p>	
	
<p>Tree transplant work for T332 to T359 has commenced, proper tree staking system and root pruning has been observed according to the method statement.</p>	<p>Tree transplant work for T332 to T359 has commenced, proper tree staking system and root pruning has been observed according to the method statement.</p>

Table 4.10 (Con't)

3. Photographic record of the transplant trees	
	
T758 transplant work has not commenced yet, crown pruning has been commenced to avoid further damaged to the tree during construction.	T758 transplant work has not commenced yet.
4. Photographic record of the night time working	
	
The lighting during night time working is confined within the working area within the site boundary. Periphery area and the sensitive receivers are not affected by the lighting during night time working.	The floodlights mounted on the boundary fence is directed inside the site boundary.



## 5. Construction Site Environmental Audit

### Site Audit

Site audit is necessary to ensure:

- No unacceptable practice on site;
- Identification of potential impacts associated with construction activities; and
- Implementation of additional mitigation measures if necessary.

Environmental Site Audit has been conducted on 28 July 2011, 4, 11, 18 and 24 August 2011.

During the reporting period, as far as the site operation was concerned, top layer PFA compaction, cut and fill operation, construction of EPC's office, piling work and excavation of sludge bunkers at plant A & B were in progress.

Regarding the air quality, access road were watered regularly by water truck or water sprinklers. Most of the site area has been covered by backfill material or coarse asphalt / aggregate. Moisture content of backfill materials and PFA stockpile had to be kept at the designed level before backfilling operation, watering was not carried out at those areas. Contractor should follow the good site practice to minimize the pulverized fuel ash from blowing up from dried surface.

With respect to water quality monitoring, two temporary water detention basins have been constructed at the North of the Lagoon near the ER's office and North-East corner of the site respectively. If there is any wastewater generated which will be pumped into the basins and will not be discharged out of the site. Construction of drainage system is in progress.

### Major Observation of Site Audit

- The contractor is reminded to increase the frequency of watering on unpaved site roads within the site and properly cover the exposed slope with tarpaulin sheeting.

### Waste Management

**C&D Waste** Backfill, piling and excavation works were conducted during the reporting period. C&D waste was generated from the current activities and sent to public fill.

**General Refuse** General refuse including paper / cardboard, metal and plastic was collected by registered collector and sent to WENT landfill.

**Chemical Waste** 120kg solid chemical waste was generated during the reporting period and collected by licensed contractor.

**Wastewater** Rain water was treated by the silt removal facilities before discharged outside the site. Waste was collected by licensed collector.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 5.1 Waste Flow Summary**

Type of Waste	Quantity Generated in Aug 2011	Cumulative quantity during construction period
Inert C&D waste	NIL	5,002.606m <sup>3</sup>
Chemical waste (Liquid)	NIL	200L
Chemical waste (Solid)	120kg	575kg
Metal	22kg	247,718kg
Paper / Cardboard Packaging	1135kg	5,156kg
Plastic	17kg	61kg
Others, e.g. general refuse	116.669m <sup>3</sup>	799.094m <sup>3</sup>

Remarks: Density of Inert C&D waste and general refuse is 1.9 tonne/m<sup>3</sup> and 1.6 tonne/m<sup>3</sup> respectively

**Impact Predication Review**

In September 2011, piling works at EEC Building, excavation at Plant A & B, substructure works at Plant A & B (include Bunker A & B construction), waterproofing works at Plant A & B, tree transplant preparation works in Portion 6, superstructure works at Plant A & B (include steel framework & truss erection), boiler assembly works, temporary transformer room construction and welfare facilities construction (include canteen, area for morning exercise) will be conducted. It is expected that these operations will not impose significant air, noise and water quality impact to the sensitive receivers. Nevertheless, necessary mitigation measures should be deployed when needed.

---

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

---

**MaterialLab****6. Summary of Complaints, Summons and Successful Prosecutions**

No complaints, summons and successful prosecutions in association with the construction activities concerning the environmental protection and pollution control were received in the reporting period.

---

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

---

**MaterialLab****7. Works Program for September 2011**

The following major construction works will be in progress in September 2011:

1. Piling works at EEC Building;
2. Excavation at Plant A & B;
3. Substructure works at Plant A & B (include Bunker A & B construction);
4. Waterproofing works at Plant A & B;
5. Tree Transplant Preparation Works in Portion 6;
6. Superstructure works at Plant A & B (include steel framework & truss erection);
7. Boiler assembly works;
8. Temporary Transformer Room construction; and
9. Welfare facilities construction (include canteen, area for morning exercise).

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****8. Monitoring Schedule for September 2011**

The monitoring schedule for September 2011 is shown in Table 8.1.

**Table 8.1 Monitoring Schedule for September 2011**

SUN	MON	TUE	WED	THU	FRI	SAT
				25 W Aug M	26	27 W M
28	29	30 W M	31	1 W Sept M	2	3 W M
4	5	6 W M	7	8 W M	9	10 W M
11	12	13 W M	14	15 W M	16	17 W M
18	19	20 W M	21	22 W M	23	24 W M
25	26	27 W M	28	29 W M	30	

Legend: W - Water quality monitoring at C1, C2, W1, W2 and W3. Three days per week.  
 M - Water quality monitoring at DM4, M1 and M2. Three days per week.

Note: Actual monitoring will be subjected to change due to any safety concern or adverse weather condition.

---

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
Fugro Development Centre, Fax : +852-2450 6138  
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

---

**9. Comments and Conclusions for the reporting period**

In this reporting period, i.e. 25 July to 24 August 2011, cut and fill operation at the foundation of treatment facilities building A & B, piling and excavation of sludge bunkers were in progress. The site activities did not lead to any significant impact to noise, air quality, stream and marine water quality.

There were 20 events of Action/Limit Level exceedances reported from 25 July to 24 August 2011. 18 events of pH exceedance were reported in the reporting period that was influent by low or high pH from upstream and heavy rain. 2 events of SS exceedance were reported in the reporting period that was due to occasional collection of dense solid particles and stirring up of seabed materials when the Deep Bay water surface became rough after Typhoon Signal No.1 was hoisted. All the events were not related to the construction activities.

Contractor shall ensure proper site practices to be implemented to avoid any deterioration of the environment around the construction site. Although there is no sensitive receivers for noise and air quality close to the site area, mitigation measures to minimize dust and noise generated from site activities should be enforced.

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**


---

### Appendix 1

#### Water Quality Monitoring Location

LOCATIONS OF STREAM  
WATER QUALITY MONITORING STATIONS

STATION	DESCRIPTION	EASTING	NORTHING
W1	IMPACT	810639.3	831296.8
W2	MONITORING	810461.6	831243.9
W3	STATION	810323.6	831196.1
C1	CONTROL	810551.0	830864.0
C2	STATION	810125.0	831084.0

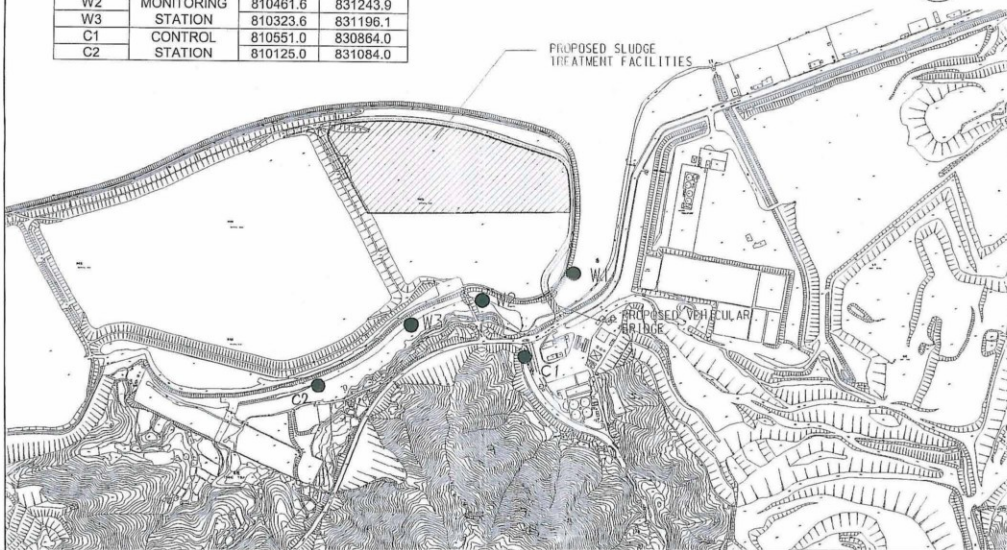

DATE: 04/05

**MAINSELL | AECOM**  
Metcalf & Eddy Ltd

AGREEMENT NO.: CE 28/2003 (EP1)  
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY  
LOCATION OF WATER QUALITY MONITORING STATIONS


(Sheet 1 of 2)

SCALE	A3 1:5000	DATE	JUN 2008
CHECK	AA/YC	DRAWN	[LMB]
DWG NO.	60039510	DRAWING NO.	FIGURE 5.1
		REV	--



LOCATIONS OF MARINE  
WATER QUALITY MONITORING STATIONS

STATION	EASTING	NORTHING
M1 (IMPACT MONITORING STATION)	809915.3	831971.6
M2 (IMPACT MONITORING STATION)	809026.4	831676.8
DM4 (CONTROL STATION)	811092.2	835181.8

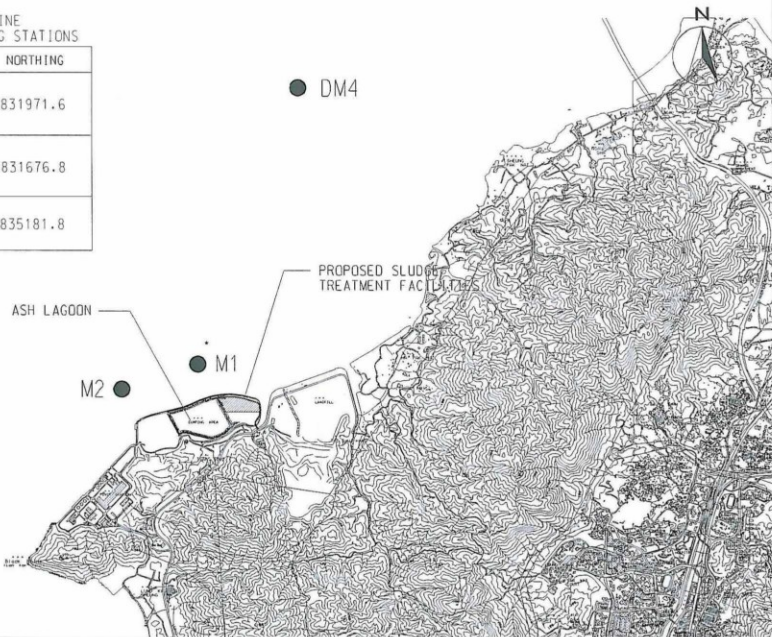

DATE: 04/24/08

**MAUNSELL** | **AECOM**  
Mitsui & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)  
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY  
LOCATION OF WATER QUALITY MONITORING STATIONS

(Sheet 2 of 2)

Sheet	A3	1:30000	Date	JUN 2008
Issue	AKYC		Drawn	[MW]
Job No.	60039510	Drawing No.	FIGURE 5.1	Rev
				-

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 2

#### Equipment Calibration Certificates

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 921438WA111242(1)



Page 1 of 2

**REPORT ON CALIBRATION OF D.O. METER****Information Supplied by Client**

Client : Fugro Technical Services Limited – MaterialLab Division –  
Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,  
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Dissolved Oxygen Meter YSI model 58

Client sample ID : Serial No. 99B0937 ( E-004-21 )

Test required : Calibration of the submitted D.O. meter

**Laboratory Information**

Lab. sample ID : WA111242/2

Date sample received : 27/06/2011

Date of calibration : 27/06/2011

Next calibration date : 27/09/2011

Test method used : Ref. Operation Manual of D.O. meter YSI model 58

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 921438WA111242(1)

Page 2 of 2

**Results:**1. Dissolved Oxygen Meter Calibration Data

Trial No.	Dissolved oxygen content, mg/L	
	By Titration	By D.O. meter
1	7.52	7.63
2	7.45	7.64
3	7.45	7.65
Average	7.47	7.64

2. Temperature

Thermometer reading, °C	Meter reading, °C
24.1	24.0

**Remark :** Dissolved oxygen content measured by the D.O. meter was found to comply with that determined by Winkler Titration. Therefore, the meter is found to be acceptable for use.

Supervised by : Y. M. ChungCertified by : Approved Signatory : HO Kin Man, John  
Manager – Chemical & EnvironmentalDate : 30/6/2011

\*\* End of Report \*\*

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk

**Materialab**

Report No. : 921438WA11219



Page 1 of 2

**REPORT ON CALIBRATION OF TURBIDIMETER****Information Supplied by Client**

Client : Fugro Technical Services Limited – Materialab Division – Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,  
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Turbidimeter, HACH Model 2100P

Client sample ID : Serial No. 010800023055 ( E-047- 13)

Test required : Calibration of the submitted Turbidimeter

**Laboratory Information**

Lab. sample ID : WA11219/1

Date sample received : 23/06/2011

Date of calibration : 23/06/2011

Next calibration date : 23/09/2011

Test method used : 

1. Three standard turbidity solutions with 20 NTU, 100 NTU and 800 NTU were prepared.
2. After the blank zero was set, the meter was calibrated against the standard solutions.
3. The gelex secondary standard with 0.00 – 9.99 NTU was inserted and the reading of this gelex standard was recorded. Same steps were repeated for 10 – 99.9 NTU and 100 – 1000 NTU gelex standards.

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiabl.com.hk

**MateriaLab**

Report No. : 921438WA111219

Page 2 of 2

**Results:**

## Calibrated Values of Secondary Gelex Standards


Auto-programmed Turbidity Standard Range	0.00-9.99 NTU, Gelex Vial	10-99.9 NTU, Gelex Vial	100-1000 NTU, Gelex Vial
Calibrated Value of the Secondary Standard, N.T.U.	4.64	58.5	541

## Checking of sample cell condition using filtered ultra-pure water

Turbidity of procedural blank, NTU	
Our sample cell	Client's sample cell
0.07	0.20

Remarks: If the reading of secondary standard was not within  $\pm 5\%$  of the calibrated value, the instrument should be recalibrated with formazin primary standards.

Supervised by : Y. M. Chung

Certified by :   
Approved Signatory : HO Kin Man, John  
Manager – Chemical & Environmental

Date : 28/6/2011

\*\*End of Report\*\*

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong

Tel: +852-2450 8233  
Fax: +852-2450 6138  
E-mail: matlab@fugro.com.hk  
Website: www.fugro.com

**MaterialLab**

Report No. : 921437CA110375

Page 1 of 1

**CALIBRATION RECORD OF WHIRLING PSYCHROMETER****Client Supplied Information**

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Calibration Item - Description : Whirling psychrometer  
Serial no. : 02586 (Dry Bulb)  
02010 (Wet Bulb)  
Equipment ID. : E-092-10

Specification limit : According to full checking report no.: 921436CA101642 , Correction at 25.0°C.  
Shall be Within -0.3 °C and 0.7 °C for dry bulb, -0.3 °C and 0.7 °C for wet bulb.

**Laboratory Information**

Calibrating Equipment - Description : Reference thermometer  
Equipment ID. : R-053-2

Date of Calibration : 15-Mar-2011 Ambient Temperature : 22 °C

Calibration location : **Calibration Laboratory of MaterialLab**Method used : **In-house Method R-C-076**In-house testing procedure no. : **R-C-076****Calibration Results :** (All values are in the unit of °C.)

Test temperature	25.0	--	--	--	--
Ref. Thermometer ID.	R-053-2	--	--	--	--
Correction of Ref. Thermometer at test temperature, C	-0.003	--	--	--	--
Variation of Ref. Thermometer reading in 20sec.	Maximum	25.003	--	--	--
	Minimum	25.000	--	--	--
Average between Max. & Min., A	25.002	--	--	--	--
Corrected temperature, (A + C), Ra	24.999	--	--	--	--
Dry Bulb	Indicated temperature, Rd	24.9	--	--	--
	Correction, Ra - Rd	0.1	--	--	--
Wet Bulb	Indicated temperature, Rw	24.8	--	--	--
	Correction, Ra - Rw	0.2	--	--	--

**Remark :**

- The equipment used in this calibration is traceable to recognized National Standards.
- The discrimination of the equipment under test is 0.1 °C ( 1/5 division).
- The equipment being calibrated does comply with the specification limit.
- Recommended next calibration date ( 6 months, In-house specification ) : 15-Sep-2011

Tested by : HC Date : 15-Mar-2011 Checked by : JC Date : 17-3-2011

C.H. Chan

CA-W-182 (30/07/98)

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 921438WA111592



Page 1 of 2

**REPORT ON CALIBRATION OF SALINITY/CONDUCTIVITY METER****Information Supplied by Client**

Client : Fugro Technical Services Limited – MaterialLab Division – Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,  
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One salinity/conductivity meter YSI model 30

Client sample ID : Serial No. 00H1322AC ( E-001-12 )

Test required : Calibration of the submitted salinity/conductivity meter

**Laboratory Information**

Lab. sample ID : WA111592/1

Date sample received : 08/08/2011

Date of calibration : 09/08/2011

Next calibration date : 09/11/2011

Test method used : Ref. Operation Manual of YSI model 30

*Note : This report refers only to the sample(s) tested.*



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 921438WA111592

Page 2 of 2

**Results:****A. Calibration of Conductivity Meter**

Temperature, °C	Conductivity, $\mu\text{mhos/cm}$			
	Theoretical	Measured	Deviation	Maximum acceptable deviation
25	-	-	-	$\pm 70$
25	-	-	-	$\pm 400$
25	-	-	-	$\pm 700$
25	-	-	-	$\pm 1200$

**B. Calibration of Salinity Meter**

Salinity, ‰			
Theoretical	Measured	Deviation	Maximum acceptable deviation
10	10.1	0.1	$\pm 0.5$
20	20.2	0.2	$\pm 1.0$
30	30.2	0.2	$\pm 1.5$
40	40.5	0.5	$\pm 2.0$

**C. Calibration of Temperature Sensor**

Thermometer Reading, °C	Meter Reading, °C	Maximum acceptable deviation, °C
24.2	24.4	$\pm 0.5$

**D. Conclusion**

The instrument is found to be acceptable for use of salinity.

Supervised by : Y. M. ChungCertified by : 

Approved Signatory : HO Kin Man, John  
Manager – Chemical & Environmental

Date : 16/8/2011**\*\* End of Report \*\***

Note : This report refers only to the sample(s) tested.

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 3

#### Stream and Marine Water Quality Monitoring Data

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 26/07/2011 (a.m.) Test No. : 102  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:34	32	0.3	30.4	11.4	8.59	121.8	13.5	8.12	17	
				30.4	11.3	8.32	117.8	13.9	8.10	19	
W2	10:15	31	0.1	30.3	8.7	6.77	93.8	8.75	7.60	10	
				30.3	9.3	6.52	91.5	8.99	7.66	10	
W3	10:53	33	0.2	31.9	5.4	8.92	125.6	19.6	7.92	36	
				31.9	5.5	9.05	127.5	21.8	7.91	46	
C1	11:11	33	0.1	32.6	0.0	10.21	141.2	5.59	8.92	3	
				32.5	0.0	10.32	142.6	5.15	8.94	4	
C2	11:28	34	0.1	31.9	1.4	9.85	135.8	2.70	8.71	2	
				31.8	1.5	10.41	143.2	2.69	8.74	1	

Certified by :

  
 Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 26/07/2011 (p.m.) Test No. : 102  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	17:54	33	0.1	31.5	10.8	10.39	149.7	16.9	8.79	21	
				31.4	10.8	10.20	146.6	16.3	8.80	22	
W2	16:29	34	0.1	32.9	4.6	8.93	127.3	25.7	8.17	30	
				32.7	4.5	8.87	125.9	26.5	8.24	28	
W3	17:04	34	0.1	31.0	3.7	9.45	129.7	5.03	8.25	8	
				31.0	3.4	9.21	126.3	5.40	8.25	5	
C1	17:38	33	0.1	30.7	0.0	9.76	130.7	5.60	9.15	4	
				30.7	0.0	9.73	130.2	5.81	9.14	5	
C2	17:22	33	0.1	30.9	0.9	9.01	121.6	2.78	8.25	2	
				30.8	0.9	8.95	120.7	2.66	8.24	2	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 28/07/2011 (a.m.) Test No. : 103  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	12:02	35	0.2	31.0	13.4	6.67	96.6	4.93	7.69	6	
				31.0	13.2	6.59	95.4	5.35	7.70	5	
W2	11:47	35	0.1	30.7	14.4	6.74	97.7	13.2	7.70	16	
				31.0	12.5	7.22	104.0	13.6	7.71	16	
W3	12:19	35	0.1	32.5	8.8	8.98	130.1	13.0	7.81	16	
				32.5	8.8	9.10	131.8	11.0	7.80	19	
C1	12:54	35	0.1	34.6	0.0	10.10	144.6	4.74	9.22	4	
				34.6	0.0	10.14	144.9	4.52	9.23	4	
C2	12:35	35	0.1	32.5	3.9	9.84	138.7	4.05	8.14	4	
				32.4	3.4	9.90	139.1	3.92	8.07	7	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 6233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 28/07/2011 (p.m.) Test No. : 103  
Tide State : MID-FLOOD Weather : RAINY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	18:02	29	0.1	30.6	14.7	6.52	94.4	14.4	7.77	120	
				30.6	14.7	6.42	93.0	14.2	7.78	130	
W2	16:35	34	0.1	31.4	7.2	8.29	116.0	24.9	7.80	37	
				31.3	7.2	8.35	117.5	24.0	7.84	43	
W3	17:14	29	0.1	28.9	5.6	6.67	89.2	29.1	7.64	39	
				28.7	5.6	6.64	88.6	29.3	7.66	39	
C1	17:40	29	0.1	30.8	0.0	9.23	123.8	31.3	8.77	74	
				30.7	0.0	9.22	123.6	27.6	8.76	31	
C2	17:28	28	0.1	29.0	2.2	6.96	91.4	4.04	7.31	3	
				29.0	2.2	6.24	82.1	3.96	7.22	3	

Certified by



Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 30/07/2011 (a.m.) Test No. : 104  
Tide State : MID-FLOOD Weather : FINE  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	8:48	30	1.0	27.4	22.4	5.56	79.7	4.43	7.63	7	
				27.5	22.4	5.40	77.4	4.64	7.66	6	
W2	10:00	31	0.1	27.5	20.1	5.34	76.3	5.15	7.62	11	
				27.6	20.0	5.30	75.9	5.00	7.61	10	
W3	9:06	30	1.0	27.8	21.0	5.56	79.6	5.93	7.73	9	
				27.8	21.0	5.36	79.8	6.08	7.73	7	
C1	9:23	32	0.1	29.3	0.0	8.95	117.1	7.23	7.67	5	
				29.4	0.0	8.84	115.8	6.62	7.60	7	
C2	9:40	31	0.1	27.5	19.6	5.26	74.4	4.57	7.39	6	
				27.5	20.0	5.22	73.9	4.23	7.46	7	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**

Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 30/07/2011 (p.m.) Test No. : 104  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:06	33	0.5	29.4	18.1	5.33	77.0	9.34	7.58	12	
				29.4	18.9	5.26	75.9	9.49	7.60	15	
W2	12:51	33	0.1	29.5	17.0	5.84	84.1	7.76	7.60	12	
				29.4	17.4	5.72	82.4	7.11	7.61	9	
W3	13:28	33	0.3	30.0	12.2	8.57	121.2	4.09	7.56	7	
				30.1	12.1	8.39	118.9	3.79	7.58	7	
C1	14:00	33	0.1	34.0	0.1	9.77	138.5	5.06	9.07	5	
				33.9	0.0	9.70	137.5	4.96	9.01	4	
C2	13:45	33	0.1	30.5	8.0	8.88	123.9	2.65	7.27	5	
				30.6	7.9	8.98	125.4	2.63	7.25	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/8/2011



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 02/08/2011 (a.m.) Test No. : 105  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	9:00	30	1.0	29.3	18.4	5.65	81.7	6.90	7.59	6	
				29.3	18.2	5.60	80.0	6.52	7.61	7	
W2	8:44	30	0.1	29.0	12.9	5.25	75.2	10.9	7.57	11	
				29.1	13.0	5.29	75.6	11.6	7.59	13	
W3	9:35	30	1.0	29.0	20.0	5.37	78.0	15.9	7.56	17	
				29.2	19.2	5.31	77.0	14.0	7.57	15	
C1	9:55	31	0.1	31.9	0.0	9.64	131.8	9.25	8.43	16	
				32.0	0.0	9.73	133.2	8.21	8.41	15	
C2	10:13	31	0.1	29.4	17.9	5.66	81.8	9.39	7.35	8	
				29.3	17.9	5.48	79.2	9.14	7.42	10	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 02/08/2011 (p.m.) Test No. : 105  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:16	34	0.5	30.2	18.3	5.25	76.7	4.83	7.58	5	
				30.2	18.5	5.32	77.4	4.70	7.60	6	
W2	14:58	34	0.1	31.2	16.7	6.75	99.8	7.91	7.62	7	
				31.2	16.7	6.36	94.1	7.60	7.63	7	
W3	15:34	32	0.4	30.6	14.6	9.82	142.3	8.18	7.75	10	
				31.0	15.7	10.38	152.2	8.53	7.86	9	
C1	16:07	34	0.1	32.8	0.0	9.73	135.1	8.43	9.37	19	
				32.7	0.0	9.75	135.0	7.94	9.30	7	
C2	15:53	33	0.1	31.1	9.6	9.66	137.3	4.57	7.37	4	
				31.1	9.5	9.79	139.2	4.51	7.35	5	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 04/08/2011 (a.m.) Test No. : 106  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:34	32	0.8	30.5	18.0	5.45	80.0	10.1	7.68	10	
				30.4	18.3	5.28	77.9	9.63	7.74	10	
W2	10:20	31	0.1	30.9	16.3	5.38	79.3	21.4	7.66	24	
				30.8	16.6	5.32	78.2	24.5	7.67	27	
W3	10:51	33	0.9	30.7	17.7	5.25	77.2	15.6	7.68	18	
				30.7	17.9	5.30	78.0	15.8	7.68	17	
C1	11:22	33	0.1	33.3	0.1	8.04	112.2	5.59	8.77	15	
				33.2	0.1	8.09	112.8	5.09	8.74	20	
C2	11:05	32	0.1	31.3	14.6	7.02	102.5	11.1	7.74	12	
				31.3	14.5	7.03	102.6	11.3	7.76	12	

Certified by :



Approved Signatory : K.M. Ho

Date :

4/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 04/08/2011 (p.m.) Test No. : 106  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:20	34	0.6	31.4	18.6	5.69	85.3	7.92	7.90	10	
				31.3	18.7	5.68	85.1	8.47	7.90	9	
W2	16:05	34	0.1	32.2	16.7	7.50	112.6	7.63	8.01	9	
				32.3	17.1	7.37	110.9	7.94	8.02	9	
W3	16:37	34	0.5	31.6	14.3	9.03	132.6	9.52	8.07	11	
				31.6	14.3	8.17	119.6	8.43	8.08	9	
C1	17:10	34	0.1	32.2	0.1	8.18	112.2	4.56	8.99	5	
				32.1	0.1	8.24	112.9	4.29	8.92	4	
C2	16:56	34	0.1	31.4	7.2	7.77	109.7	2.54	7.58	2	
				31.4	7.1	7.81	110.9	2.62	7.60	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

4/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk

**MateriaLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 06/08/2011 (a.m.) Test No. : 107  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:42	34	0.4	32.2	19.4	6.98	106.6	21.1	7.74	21	
				32.1	19.5	7.13	108.7	20.1	7.78	22	
W2	12:49	34	0.1	32.6	18.9	6.05	92.7	18.8	7.62	20	
				32.9	18.7	6.24	96.0	20.0	7.64	20	
W3	11:58	34	0.4	33.7	13.4	7.80	118.1	27.7	7.73	29	
				33.7	13.4	7.55	114.4	26.5	7.71	32	
C1	12:36	34	0.1	35.5	0.0	10.13	146.6	5.26	9.11	9	
				35.4	0.0	10.26	148.7	5.49	9.09	13	
C2	12:16	34	0.1	34.8	4.3	10.90	160.2	3.18	8.14	3	
				34.8	4.4	10.64	156.3	3.09	8.13	3	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

15/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 06/08/2011 (p.m.) Test No. : 107  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:38	33	0.7	32.7	19.3	7.77	119.4	4.93	7.93	6	
				32.6	19.2	7.64	117.3	5.23	7.92	6	
W2	16:22	34	0.1	33.4	19.5	7.93	123.4	8.31	8.04	10	
				33.4	19.4	8.07	125.6	8.01	8.05	9	
W3	16:54	33	0.7	32.9	19.1	7.51	115.8	8.82	7.97	9	
				32.9	19.2	7.40	114.0	8.76	7.96	9	
C1	17:26	34	0.1	32.1	0.0	7.92	108.6	18.2	9.21	17	
				32.1	0.0	7.85	107.6	17.0	9.20	17	
C2	17:11	33	0.1	33.2	3.6	8.78	125.0	3.69	8.04	4	
				33.1	3.6	8.67	123.2	3.34	7.93	4	

Certified by :



Approved Signatory : K.M. Ho

Date :

15/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 09/08/2011 (a.m.) Test No. : 108  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:13	28	0.3	29.3	16.9	5.43	76.3	11.4	7.41	14	
				29.1	16.7	5.50	76.7	11.5	7.43	12	
W2	9:41	28	0.1	28.9	13.5	5.20	72.3	14.2	7.11	14	
				29.0	14.1	5.26	73.4	13.6	7.12	15	
W3	9:55	28	0.4	29.0	12.0	5.25	73.0	10.9	7.13	14	
				29.0	12.0	5.34	74.2	10.5	7.15	12	
C1	10:45	30	0.1	29.6	0.0	7.36	97.6	999>	8.81	2600	
				29.8	0.0	6.41	85.2	999>	8.63	1900	
C2	11:05	30	0.1	29.1	4.0	6.95	92.2	10.1	7.22	7	
				28.9	4.0	6.73	89.0	10.4	7.19	8	

Certified by :

  
 Approved Signatory : K.M. Ho

Date :

15/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 09/08/2011 (p.m.) Test No. : 108  
Tide State : MID-FLOOD Weather : CLOUDY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	17:01	30	0.1	29.8	17.2	7.69	111.4	22.1	7.78	20	
				29.9	17.2	7.34	106.5	23.0	7.81	24	
W2	16:35	29	0.1	28.9	7.7	8.85	120.9	26.9	7.71	35	
				29.0	7.7	8.57	116.2	25.3	7.75	28	
W3	18:01	29	0.1	28.7	7.2	8.14	109.5	6.91	7.70	7	
				28.7	7.0	8.32	112.0	7.65	7.72	9	
C1	17:32	28	0.1	28.8	0.0	8.47	109.0	10.6	8.00	10	
				28.9	0.0	8.35	107.0	10.7	7.98	13	
C2	17:18	28	0.1	28.8	5.0	9.07	120.9	6.03	7.62	7	
				28.8	5.0	8.94	119.1	5.78	7.57	6	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

15/8/2011



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 11/08/2011 (a.m.) Test No. : 109  
Tide State : MID-EBB Weather : FINE  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:55	33	0.4	29.8	18.2	5.26	75.6	15.2	7.44	26	
				29.8	18.1	5.34	76.7	14.0	7.46	19	
W2	11:32	32	0.1	29.5	10.8	6.74	93.9	8.21	7.22	10	
				29.5	10.5	6.34	88.1	8.39	7.25	11	
W3	12:13	32	0.2	30.9	7.4	7.34	102.7	5.91	7.39	9	
				31.0	7.3	7.24	101.3	6.28	7.36	10	
C1	12:47	33	0.1	30.0	0.0	7.80	103.2	9.55	7.21	4	
				30.0	0.0	7.81	103.4	9.67	7.09	4	
C2	12:29	33	0.1	29.7	7.1	7.57	103.4	4.32	7.08	8	
				29.7	6.8	7.62	104.3	4.09	7.07	7	

Certified by, :



Approved Signatory : K.M. Ho

Date :

18/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**


Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**Project : **Contract No. EP/SP/58/08****Field Data Record (Stream Water)**

Date : 11/08/2011 (p.m.) Test No. : 109  
Tide State : MID-FLOOD Weather : FINE  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	17:10	32	0.1	29.3	21.0	5.58	81.9	19.1	7.61	21	
				29.2	21.1	5.46	80.0	19.0	7.65	20	
W2	16:55	33	0.1	29.1	5.3	7.48	100.3	17.1	7.22	25	
				29.1	5.4	7.23	97.0	15.5	7.24	24	
W3	17:26	32	0.1	28.6	5.9	6.89	92.0	3.78	7.24	5	
				28.6	5.8	6.85	91.3	3.87	7.19	5	
C1	17:57	31	0.1	28.7	0.0	7.10	91.7	9.07	7.27	4	
				28.7	0.0	7.03	90.8	9.19	7.17	3	
C2	17:42	31	0.1	28.2	1.7	6.22	80.4	4.72	7.07	3	
				28.2	1.7	6.12	79.2	4.51	7.03	2	

Certified by :



Approved Signatory : K.M. Ho

Date :

18/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 13/08/2011 (a.m.) Test No. : 110  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	8:58	32	1.0	29.6	19.1	5.44	79.2	4.00	7.59	3	
				29.6	19.1	5.40	78.7	3.64	7.60	4	
W2	8:38	30	0.1	29.6	18.6	5.64	82.2	8.39	7.57	9	
				29.6	18.9	5.50	80.0	7.88	7.59	11	
W3	9:14	31	1.0	30.3	17.1	5.39	79.7	7.31	7.59	8	
				30.3	17.1	5.32	77.7	6.93	7.62	7	
C1	9:50	33	0.1	29.4	0.0	8.23	107.7	6.82	8.07	4	
				29.4	0.0	8.16	106.7	6.43	7.90	2	
C2	9:32	31	0.1	29.3	15.7	5.30	76.3	4.53	7.32	6	
				29.3	15.7	5.26	75.8	4.92	7.29	7	

Certified by :



Approved Signatory : K.M. Ho

Date :

21/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**

Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 13/08/2011 (p.m.) Test No. : 110  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:21	33	0.3	30.0	18.5	5.25	77.0	24.1	7.62	34	
				29.9	18.4	5.32	78.0	26.4	7.63	38	
W2	13:06	34	0.1	31.5	14.7	5.80	86.2	10.3	7.60	14	
				31.6	14.3	5.53	81.3	10.1	7.59	14	
W3	13:38	33	0.2	32.1	10.9	7.42	108.0	6.48	7.57	10	
				32.2	10.8	7.56	110.2	5.93	7.56	12	
C1	14:13	33	0.1	33.9	0.0	7.60	107.3	6.77	8.78	5	
				33.8	0.0	7.49	105.6	6.94	8.73	6	
C2	13:57	33	0.1	32.3	4.9	8.41	118.8	3.31	7.61	4	
				32.3	4.9	8.33	117.6	3.48	7.60	4	

Certified by :



Approved Signatory : K.M. Ho

Date :

21/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 16/08/2011 (a.m.) Test No. : 111  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	9:22	30	1.0	30.2	18.6	5.71	84.1	6.49	7.64	7	
				30.2	18.6	5.44	80.0	6.73	7.64	6	
W2	8:40	30	0.1	30.1	15.5	5.70	82.3	17.3	7.42	13	
				30.0	15.8	5.68	82.0	16.7	7.43	20	
W3	9:05	30	1.0	30.2	16.2	5.51	79.7	15.3	7.50	15	
				30.2	16.1	5.25	76.2	13.7	7.51	17	
C1	9:42	31	0.1	29.8	0.0	9.75	128.7	5.54	8.34	3	
				30.1	0.0	9.63	127.7	5.01	8.18	3	
C2	10:18	31	0.1	30.6	15.9	7.32	106.7	9.33	7.49	9	
				30.6	15.8	7.22	105.3	9.00	7.49	8	

Certified by :



Approved Signatory : K.M. Ho

Date :

21/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**

Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 16/08/2011 (p.m.) Test No. : 111  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:03	33	0.4	32.1	17.4	6.34	95.5	17.2	7.71	19	
				32.0	17.4	6.22	93.5	16.7	7.71	18	
W2	14:47	33	0.1	32.6	14.7	8.72	130.6	17.5	7.81	17	
				32.7	14.7	8.39	125.7	15.4	7.84	18	
W3	15:19	33	0.2	32.1	10.7	8.45	122.9	6.43	7.89	10	
				32.0	10.8	8.92	129.5	5.90	7.85	10	
C1	15:53	33	0.1	33.2	0.0	10.13	141.3	5.78	9.75	8	
				33.1	0.0	10.22	142.4	5.67	9.74	7	
C2	15:36	33	0.1	32.5	4.9	8.93	126.7	3.51	7.81	3	
				32.5	4.8	9.16	129.8	3.34	7.80	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

28/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 18/08/2011 (a.m.) Test No. : 112  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:15	33	0.9	30.5	19.6	6.61	98.1	11.3	7.76	10	
				30.6	19.2	6.29	93.4	10.2	7.76	9	
W2	9:54	33	0.1	30.6	16.3	5.69	83.1	21.1	7.62	21	
				30.6	16.4	5.74	83.9	19.9	7.64	16	
W3	10:31	33	0.8	30.7	16.6	5.71	83.9	17.1	7.59	20	
				30.7	16.6	5.61	82.3	16.1	7.58	22	
C1	11:03	34	0.1	34.0	0.0	8.05	113.6	9.29	9.40	7	
				34.0	0.0	8.25	116.0	7.93	9.35	6	
C2	10:46	33	0.1	30.6	11.0	8.82	125.2	10.2	7.70	10	
				30.6	11.0	8.63	122.5	9.29	7.68	10	

Certified by :

  
 Approved Signatory : K.M. Ho

Date :

28/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 18/08/2011 (p.m.) Test No. : 112  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:53	33	0.4	31.3	18.0	7.99	119.3	21.5	7.93	28	
				31.8	17.9	8.11	121.9	22.7	8.00	36	
W2	15:38	33	0.1	32.8	15.1	8.24	124.0	14.3	7.84	18	
				32.8	15.1	8.09	121.7	13.3	7.87	16	
W3	16:11	33	0.2	31.5	9.6	7.92	113.3	7.35	7.95	9	
				31.5	9.6	7.88	112.8	6.93	7.94	10	
C1	16:45	33	0.1	31.9	0.1	8.30	113.4	171	9.24	140	
				31.8	0.0	8.26	112.9	194	9.26	120	
C2	16:26	33	0.1	31.1	3.1	8.81	120.7	3.20	7.91	3	
				31.0	3.0	8.90	121.9	3.02	7.84	2	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

28/8/2011



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 20/08/2011 (a.m.) Test No. : 113  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:12	33	0.4	30.8	19.1	7.03	104.7	18.7	7.73	23	Red Tide
				30.9	19.1	6.74	100.6	16.2	7.81	17	
W2	11:45	33	0.1	31.9	16.9	6.56	98.3	21.3	7.67	20	
				31.6	17.2	6.49	96.9	23.1	7.68	23	
W3	11:30	34	0.5	31.5	14.4	5.53	81.3	19.7	7.60	19	
				31.5	14.5	5.68	83.4	19.1	7.61	19	
C1	12:18	32	0.1	31.5	0.1	10.25	139.1	6.61	9.57	3	
				31.5	0.1	10.05	136.4	6.43	9.50	5	
C2	12:00	32	0.1	31.3	2.5	10.03	137.6	3.90	8.06	2	
				31.2	2.5	9.93	136.0	3.53	8.00	1	

Certified by :



Approved Signatory : K.M. Ho

Date :

20/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 20/08/2011 (p.m.) Test No. : 113  
Tide State : MID-EBB Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:33	34	0.3	31.1	19.2	6.63	99.3	8.61	7.94	12	Red Tide
				30.9	19.0	6.53	98.0	8.90	7.90	11	
W2	16:13	34	0.1	32.7	14.5	7.91	118.6	15.0	7.96	20	
				32.6	14.8	7.83	117.4	15.3	7.95	18	
W3	16:50	34	0.3	32.6	9.6	9.70	141.5	17.1	8.12	25	
				32.6	9.5	9.48	138.1	15.0	8.13	20	
C1	17:25	32	0.1	29.9	0.0	9.21	121.6	7.69	9.15	11	
				30.0	0.0	9.02	119.0	7.28	9.10	9	
C2	17:05	33	0.1	31.1	1.6	8.87	120.7	3.43	8.12	3	
				31.1	1.6	8.83	120.1	3.21	7.96	2	

Certified by :



Approved Signatory : K.M. Ho

Date :

20/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 23/08/2011 (a.m.) Test No. : 114  
Tide State : MID-EBB Weather : CLOUDY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	9:13	30	0.2	30.0	14.4	7.58	108.5	11.2	7.98	12	
				29.9	14.4	7.16	102.4	12.3	7.98	10	
W2	8:40	30	0.1	29.8	14.8	5.34	76.4	10.7	7.19	7	
				29.8	14.7	5.43	77.6	9.30	7.26	12	
W3	9:38	30.5	0.1	31.6	8.7	10.42	148.7	6.23	8.15	11	
				31.5	9.0	10.62	151.5	5.57	8.13	13	
C1	9:58	31	0.1	29.4	0.0	9.93	130.0	6.55	8.85	3	
				29.3	0.0	10.22	133.6	5.87	9.01	4	
C2	10:23	31	0.1	30.3	3.1	9.92	134.2	2.58	7.72	2	
				30.2	3.1	9.80	132.8	2.73	7.76	1	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

31/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN111342

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Stream Water)**

Date : 23/08/2011 (p.m.) Test No. : 114  
Tide State : MID-FLOOD Weather : SUNNY  
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:31	33	0.1	33.3	15.1	9.02	136.9	26.0	8.28	29	
				33.3	15.1	8.69	131.8	27.6	8.28	31	
W2	15:15	34	0.1	36.4	11.0	6.32	98.6	27.5	7.81	31	
				36.4	11.2	6.37	99.5	24.0	7.84	27	
W3	15:53	32	0.1	33.0	7.8	8.85	128.3	21.3	8.42	21	
				32.9	7.8	8.39	121.8	19.0	8.39	27	
C1	16:33	33	0.1	31.8	0.0	9.19	125.3	6.03	9.69	8	
				31.8	0.0	9.34	127.3	7.07	9.60	5	
C2	16:13	33	0.1	32.6	1.4	9.56	133.3	3.27	8.71	2	
				32.6	1.5	9.75	135.9	3.02	8.69	2	

Certified by :



Approved Signatory : K.M. Ho

Date :

31/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(10)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 26/07/2011

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111267(10)/1 – WA111267(10)/20

Date of receipt of sample : 26/07/2011

Date test commenced : 27/07/2011

Date test completed : 28/07/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111267(10)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	3
2. C1 AE	4
3. C2 AE	2
4. C2 AE	1
5. W1 AE	17
6. W1 AE	19
7. W2 AE	10
8. W2 AE	10
9. W3 AE	36
10. W3 AE	46
11. C1 PF	4
12. C1 PF	5
13. C2 PF	2
14. C2 PF	2
15. W1 PF	21
16. W1 PF	22
17. W2 PF	30
18. W2 PF	28
19. W3 PF	8
20. W3 PF	5

Supervised by : Y. M. Chung
 Certified by   
 Approved Signatory : HO Kin Man, John  
 Manager - Chemical & Environmental
Date : 9/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Scheme (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(10)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	22	22

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(11)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 28/07/2011

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111267(11)/1 – WA111267(11)/20

Date of receipt of sample : 28/07/2011

Date test commenced : 29/07/2011

Date test completed : 30/07/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
APHA 17ed. 2540D

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.



**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk


**MateriaLab**

Report No. : 100440WA111267(11)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	4
2. C1 AE	4
3. C2 AE	4
4. C2 AE	7
5. W1 AE	6
6. W1 AE	5
7. W2 AE	16
8. W2 AE	16
9. W3 AE	16
10. W3 AE	19
11. C1 PF	74
12. C1 PF	31
13. C2 PF	3
14. C2 PF	3
15. W1 PF	120
16. W1 PF	130
17. W2 PF	37
18. W2 PF	43
19. W3 PF	39
20. W3 PF	39

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 10/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(11)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W3 PF	39	40

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	105

*Note : This report refers only to the sample(s) tested.*

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8238  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

# MaterialLab

Report No. : 100440WA111267(12)



Page 1 of 2

### TEST REPORT ON ANALYSIS OF WATER

#### Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture  
Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.  
Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme  
Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 30/07/2011  
Client sample ID :  
1. C1 AF  
2. C1 AF  
3. C2 AF  
4. C2 AF  
5. W1 AF  
6. W1 AF  
7. W2 AF  
8. W2 AF  
9. W3 AF  
10. W3 AF  
11. C1 PE  
12. C1 PE  
13. C2 PE  
14. C2 PE  
15. W1 PE  
16. W1 PE  
17. W2 PE  
18. W2 PE  
19. W3 PE  
20. W3 PE  
Test required : Total suspended solids dried at 103°C – 105°C

#### Laboratory Information

Lab. sample ID : WA111267(12)/1 – WA111267(12)/20  
Date of receipt of sample : 30/07/2011  
Date test commenced : 01/08/2011  
Date test completed : 02/08/2011  
Test method used : Total suspended solids dried at 103°C – 105°C  
APHA 17ed. 2540D

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(12)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	5
2. C1 AF	7
3. C2 AF	6
4. C2 AF	7
5. W1 AF	7
6. W1 AF	6
7. W2 AF	11
8. W2 AF	10
9. W3 AF	9
10. W3 AF	7
11. C1 PE	5
12. C1 PE	4
13. C2 PE	5
14. C2 PE	3
15. W1 PE	12
16. W1 PE	15
17. W2 PE	12
18. W2 PE	9
19. W3 PE	7
20. W3 PE	7

Supervised by : Y. M. Chung
 Certified by:   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 10/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Scheme (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111267(12)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
-	-	-

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	96

*Note : This report refers only to the sample(s) tested.*

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

# MaterialLab

Report No. : 100440WA111538



Page 1 of 2

## TEST REPORT ON ANALYSIS OF WATER

### Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 02/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

### Laboratory Information

Lab. sample ID : WA111538/1 – WA111538/20

Date of receipt of sample : 02/08/2011

Date test commenced : 03/08/2011

Date test completed : 04/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

Materialab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk


**Materialab**

Report No. : 100440WA111538

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	16
2. C1 AF	15
3. C2 AF	8
4. C2 AF	10
5. W1 AF	6
6. W1 AF	7
7. W2 AF	11
8. W2 AF	13
9. W3 AF	17
10. W3 AF	15
11. C1 PE	19
12. C1 PE	7
13. C2 PE	4
14. C2 PE	5
15. W1 PE	5
16. W1 PE	6
17. W2 PE	7
18. W2 PE	7
19. W3 PE	10
20. W3 PE	9

Supervised by : Y. M. Chung
 Certified by   
 Approved Signatory : HO Kin Man, John  
 Manager - Chemical & Environmental
Date : 9/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
C1 PE	7	7

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	105

*Note : This report refers only to the sample(s) tested.*



## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

# MaterialLab

Report No. : 100440WA111538(1)



Page 1 of 2

### TEST REPORT ON ANALYSIS OF WATER

#### Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 04/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

#### Laboratory Information

Lab. sample ID : WA111538(1)/1 – WA111538(1)/20

Date of receipt of sample : 04/08/2011

Date test commenced : 05/08/2011

Date test completed : 06/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
APHA 17ed. 2540D

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(1)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	15
2. C1 AF	20
3. C2 AF	12
4. C2 AF	12
5. W1 AF	10
6. W1 AF	10
7. W2 AF	24
8. W2 AF	27
9. W3 AF	18
10. W3 AF	17
11. C1 PE	5
12. C1 PE	4
13. C2 PE	2
14. C2 PE	3
15. W1 PE	10
16. W1 PE	9
17. W2 PE	9
18. W2 PE	9
19. W3 PE	11
20. W3 PE	9

Supervised by : Y. M. Chung
 Certified by   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 10/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by the laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(1)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 AF	29	25

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	98

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(2)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 06/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(2)/1 – WA111538(2)/20

Date of receipt of sample : 06/08/2011

Date test commenced : 07/08/2011

Date test completed : 08/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HKLAS) for specific laboratory activities as listed in the HKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(2)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	9
2. C1 AF	13
3. C2 AF	3
4. C2 AF	3
5. W1 AF	21
6. W1 AF	22
7. W2 AF	20
8. W2 AF	20
9. W3 AF	29
10. W3 AF	32
11. C1 PE	17
12. C1 PE	17
13. C2 PE	4
14. C2 PE	4
15. W1 PE	6
16. W1 PE	6
17. W2 PE	10
18. W2 PE	9
19. W3 PE	9
20. W3 PE	9

Supervised by : Y. M. Chung
 Certified by:   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 15/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by the laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(2)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W3 AF	32	32

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
 Fugro Development Centre,  
 5 Lok Yi Street, 17 M.S. Castle Peak Road,  
 Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
 Fax : +852-2450 6138  
 E-mail : matlab@fugro.com.hk  
 Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(3)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 09/08/2011

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(3)/1 – WA111538(3)/20

Date of receipt of sample : 09/08/2011

Date test commenced : 10/08/2011

Date test completed : 11/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(3)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	2600
2. C1 AE	1900
3. C2 AE	7
4. C2 AE	8
5. W1 AE	14
6. W1 AE	12
7. W2 AE	14
8. W2 AE	15
9. W3 AE	14
10. W3 AE	12
11. C1 PF	10
12. C1 PF	13
13. C2 PF	7
14. C2 PF	6
15. W1 PF	20
16. W1 PF	24
17. W2 PF	35
18. W2 PF	28
19. W3 PF	7
20. W3 PF	9

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 15/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.



**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiabl.com.hk

**MateriaLab**

Report No. : 100440WA111538(3)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	25	24

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	95

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(4)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 11/08/2011

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(4)/1 – WA111538(4)/20

Date of receipt of sample : 11/08/2011

Date test commenced : 12/08/2011

Date test completed : 13/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HKLAS) for specific laboratory activities as listed in the HKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(4)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	4
2. C1 AE	4
3. C2 AE	8
4. C2 AE	7
5. W1 AE	26
6. W1 AE	19
7. W2 AE	10
8. W2 AE	11
9. W3 AE	9
10. W3 AE	10
11. C1 PF	4
12. C1 PF	3
13. C2 PF	3
14. C2 PF	2
15. W1 PF	21
16. W1 PF	20
17. W2 PF	25
18. W2 PF	24
19. W3 PF	5
20. W3 PF	5

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 15/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(4)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	20	19

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102

*Note : This report refers only to the sample(s) tested.*

# FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiialab.com.hk

# MateriaLab

Report No. : 100440WA111538(5)



Page 1 of 2

## TEST REPORT ON ANALYSIS OF WATER

### Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MateriaLab on 13/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

### Laboratory Information

Lab. sample ID : WA111538(5)/1 – WA111538(5)/20

Date of receipt of sample : 13/08/2011

Date test commenced : 15/08/2011

Date test completed : 16/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
APHA 17ed. 2540D

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : mallab@fugro.com.hk  
Website : www.materialab.com.hk


**MateriaLab**

Report No. : 100440WA111538(5)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	4
2. C1 AF	2
3. C2 AF	6
4. C2 AF	7
5. W1 AF	3
6. W1 AF	4
7. W2 AF	9
8. W2 AF	11
9. W3 AF	8
10. W3 AF	7
11. C1 PE	5
12. C1 PE	6
13. C2 PE	4
14. C2 PE	4
15. W1 PE	34
16. W1 PE	38
17. W2 PE	14
18. W2 PE	14
19. W3 PE	10
20. W3 PE	12

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory: HO Kin Man, John  
 Mahager – Chemical & Environmental
Date : 20/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk

**MateriaLab**

Report No. : 100440WA111538(5)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PE	37	39

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	103

*Note : This report refers only to the sample(s) tested.*

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mui, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

# MaterialLab

Report No. : 100440WA111538(6)



Page 1 of 2

### TEST REPORT ON ANALYSIS OF WATER

#### Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 16/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

#### Laboratory Information

Lab. sample ID : WA111538(6)/1 – WA111538(6)/20

Date of receipt of sample : 16/08/2011

Date test commenced : 16/08/2011

Date test completed : 18/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(6)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	3
2. C1 AF	3
3. C2 AF	9
4. C2 AF	8
5. W1 AF	7
6. W1 AF	6
7. W2 AF	13
8. W2 AF	20
9. W3 AF	15
10. W3 AF	17
11. C1 PE	8
12. C1 PE	7
13. C2 PE	3
14. C2 PE	3
15. W1 PE	19
16. W1 PE	18
17. W2 PE	17
18. W2 PE	18
19. W3 PE	10
20. W3 PE	10

Supervised by : Y. M. Chung
 Certified by:   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 15/8/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(6)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PE	18	18

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	94

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(7)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheung Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 18/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(7)/1 – WA111538(7)/20

Date of receipt of sample : 18/08/2011

Date test commenced : 18/08/2011

Date test completed : 20/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(7)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	7
2. C1 AF	6
3. C2 AF	10
4. C2 AF	10
5. W1 AF	10
6. W1 AF	9
7. W2 AF	21
8. W2 AF	16
9. W3 AF	20
10. W3 AF	22
11. C1 PE	140
12. C1 PE	120
13. C2 PE	3
14. C2 PE	2
15. W1 PE	28
16. W1 PE	36
17. W2 PE	18
18. W2 PE	16
19. W3 PE	9
20. W3 PE	10

Supervised by : Y. M. Chung
 Certified by : [Signature]  
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 23/8/11

\*\*End of Report\*\*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(7)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 PE	17	16

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	99

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 8138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(8)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 20/08/2011

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(8)/1 – WA111538(8)/20

Date of receipt of sample : 20/08/2011

Date test commenced : 22/08/2011

Date test completed : 23/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
*APHA 17ed. 2540D*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HKLAS) for specific laboratory activities as listed in the HKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(8)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	3
2. C1 AF	5
3. C2 AF	2
4. C2 AF	1
5. W1 AF	23
6. W1 AF	17
7. W2 AF	20
8. W2 AF	23
9. W3 AF	19
10. W3 AF	19
11. C1 PE	11
12. C1 PE	9
13. C2 PE	3
14. C2 PE	2
15. W1 PE	12
16. W1 PE	11
17. W2 PE	20
18. W2 PE	18
19. W3 PE	25
20. W3 PE	20

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory : HO Kin Man, John  
 Manager - Chemical & Environmental
Date : 24/8/11

\*\*End of Report\*\*

*Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(8)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 PE	18	19

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	101

*Note : This report refers only to the sample(s) tested.*



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(9)



Page 1 of 2

**TEST REPORT ON ANALYSIS OF WATER****Information Supplied by Client**

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : Level 30, Tower 1, Kowloon Commerce Centre, 51 Kwai Cheong Road, Kwai Chung, N.T.

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 23/08/2011

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

**Laboratory Information**

Lab. sample ID : WA111538(9)/1 – WA111538(9)/20

Date of receipt of sample : 23/08/2011

Date test commenced : 23/08/2011

Date test completed : 25/08/2011

Test method used : Total suspended solids dried at 103°C – 105°C  
APHA 17ed. 2540D

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk


**MaterialLab**

Report No. : 100440WA111538(9)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	3
2. C1 AE	4
3. C2 AE	2
4. C2 AE	1
5. W1 AE	12
6. W1 AE	10
7. W2 AE	7
8. W2 AE	12
9. W3 AE	11
10. W3 AE	13
11. C1 PF	8
12. C1 PF	5
13. C2 PF	2
14. C2 PF	2
15. W1 PF	29
16. W1 PF	31
17. W2 PF	31
18. W2 PF	27
19. W3 PF	21
20. W3 PF	27

Supervised by : Y. M. Chung
 Certified by :   
 Approved Signatory : HO Kin Man, John  
 Manager – Chemical & Environmental
Date : 2/9/2011**\*\*End of Report\*\****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Report No. : 100440WA111538(9)

**Laboratory Duplicate Result**

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	30	32

**Laboratory Blank**

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

**Laboratory QC sample**

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	99

*Note : This report refers only to the sample(s) tested.*

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 26/07/2011 (a.m.)

Test No. : 79


Tide State : MID-EBB

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:55	31	3.5	S	1.0	30.6	< 0.5	< 1	< 20	
						30.6	< 0.5	< 1	< 20	
				B	2.5	30.6	< 0.5	< 1	< 20	
30.6	< 0.5	< 1	< 20							
M2	10:41	31	4.9	S	1.0	30.5	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
				B	3.9	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
DM4	11:13	31	4.3	S	1.0	30.6	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	
				B	3.3	30.6	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : mallab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 26/07/2011 (p.m.) Test No. : 79  
Tide State : MID-FLOOD Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	17:05	32	3.1	S	1.0	30.9	< 0.5	< 1	< 20	
						30.9	< 0.5	< 1	< 20	
				B	2.1	30.7	< 0.5	< 1	< 20	
						30.6	< 0.5	< 1	< 20	
M2	16:52	33	5.0	S	1.0	31.0	< 0.5	< 1	< 20	
						31.0	< 0.5	< 1	< 20	
				B	4.0	29.0	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
DM4	17:26	32	4.1	S	1.0	31.7	< 0.5	< 1	< 20	
						31.7	< 0.5	< 1	< 20	
				B	3.1	30.6	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

19/7/11

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 28/07/2011 (a.m.) Test No. : 80  
Tide State : MID-EBB Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	12:18	33	3.3	S	1.0	30.3	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	2.3	28.5	< 0.5	< 1	< 20	
						28.4	< 0.5	< 1	< 20	
M2	12:06	33	5.1	S	1.0	30.4	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
				B	4.1	27.5	< 0.5	< 1	< 20	
						27.6	< 0.5	< 1	< 20	
DM4	12:37	33	4.3	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	3.3	28.2	< 0.5	< 1	< 20	
						28.0	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 30/07/2011 (a.m.) Test No. : 81  
Tide State : MID-FLOOD Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:05	30	4.4	S	1.0	27.2	< 0.5	< 1	< 20	
						27.1	< 0.5	< 1	< 20	
				B	3.4	26.8	< 0.5	< 1	< 20	
						26.9	< 0.5	< 1	< 20	
M2	8:53	30	5.8	S	1.0	27.1	< 0.5	< 1	< 20	
						27.2	< 0.5	< 1	< 20	
				B	4.8	27.0	< 0.5	< 1	< 20	
						27.0	< 0.5	< 1	< 20	
DM4	9:25	30	5.6	S	1.0	26.7	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
				B	4.6	26.5	< 0.5	< 1	< 20	
						26.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 30/07/2011 (p.m.) Test No. : 81  
Tide State : MID-EBB Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	13:20	32	3.9	S	1.0	28.2	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
				B	2.9	27.9	< 0.5	< 1	< 20	
						28.0	< 0.5	< 1	< 20	
M2	13:07	32	5.3	S	1.0	28.1	< 0.5	< 1	< 20	
						28.0	< 0.5	< 1	< 20	
				B	4.3	27.6	< 0.5	< 1	< 20	
						27.5	< 0.5	< 1	< 20	
DM4	13:40	32	4.8	S	1.0	28.1	< 0.5	< 1	< 20	
						28.1	< 0.5	< 1	< 20	
				B	3.8	27.4	< 0.5	< 1	< 20	
						27.4	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

31/7/11



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 02/08/2011 (a.m.)

Test No. : 82


Tide State : MID-FLOOD

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:17	30	4.4	S	1.0	28.5	< 0.5	< 1	< 20	
						28.4	< 0.5	< 1	< 20	
				B	3.4	27.9	< 0.5	< 1	< 20	
						27.9	< 0.5	< 1	< 20	
M2	9:04	30	5.8	S	1.0	28.5	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	
				B	4.8	28.2	< 0.5	< 1	< 20	
						28.1	< 0.5	< 1	< 20	
DM4	9:38	31	5.4	S	1.0	28.3	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
				B	4.4	28.1	< 0.5	< 1	< 20	
						28.1	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

19/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 02/08/2011 (p.m.)

Test No. : 82


Tide State : MID-EBB

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	15:34	33	3.7	S	1.0	29.7	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	2.7	29.6	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
M2	15:20	33	5.6	S	1.0	30.7	< 0.5	< 1	< 20	
						30.8	< 0.5	< 1	< 20	
				B	4.6	29.3	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
DM4	15:53	32	4.4	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	3.4	29.4	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 04/08/2011 (a.m.)

Test No. : 83


Tide State : MID-FLOOD

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:50	31	3.9	S	1.0	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
				B	2.9	29.1	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
M2	10:36	31	5.7	S	1.0	29.8	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	4.7	29.3	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
DM4	11:10	31	5.0	S	1.0	29.3	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
				B	4.0	29.0	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

11/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 04/08/2011 (p.m.) Test No. : 83  
Tide State : MID-EBB Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:46	32	3.3	S	1.0	30.2	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	2.3	30.2	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
M2	16:33	32	5.1	S	1.0	31.3	< 0.5	< 1	< 20	
						31.2	< 0.5	< 1	< 20	
				B	4.1	30.6	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
DM4	17:07	32	4.7	S	1.0	30.5	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
				B	3.7	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 06/08/2011 (a.m.)

Test No. : 84


Tide State : MID-FLOOD

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	11:57	33	3.2	S	1.0	30.2	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	2.2	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
M2	11:44	33	4.9	S	1.0	30.4	< 0.5	< 1	< 20	Filling Work
						30.3	< 0.5	< 1	< 20	
				B	3.9	29.8	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
DM4	12:16	33	4.8	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	3.8	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : **VW-VES (HK) Ltd.**


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 06/08/2011 (p.m.) Test No. : 84  
Tide State : MID-EBB Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:53	33	3.5	S	1.0	30.4	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
				B	2.5	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
M2	16:41	33	5.2	S	1.0	30.6	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
				B	4.2	30.3	< 0.5	< 1	< 20	
						30.3	< 0.5	< 1	< 20	
DM4	17:12	33	4.6	S	1.0	30.5	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
				B	3.6	30.3	< 0.5	< 1	< 20	
						30.3	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

11/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 09/08/2011 (a.m.)

Test No. : 85


Tide State : MID-EBB

Weather : CLOUDY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:38	29	3.3	S	1.0	29.1	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
				B	2.3	28.8	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
M2	10:23	28	5.5	S	1.0	29.4	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
				B	4.5	29.0	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
DM4	10:56	29	4.1	S	1.0	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	3.1	29.3	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

19/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 09/08/2011 (a.m.)

Test No. : 85


Tide State : MID-FLOOD

Weather : CLOUDY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	17:12	29	3.1	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	2.1	29.6	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
M2	17:00	29	4.7	S	1.0	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	3.7	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
DM4	17:31	29	4.2	S	1.0	29.9	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	3.2	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

19/2011



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 11/08/2011 (a.m.)

Test No. : 86


Tide State : MID-EBB

Weather : FINE

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	12:14	32	3.7	S	1.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	2.7	28.6	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	
M2	12:00	33	4.4	S	1.0	29.5	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
				B	3.4	28.9	< 0.5	< 1	< 20	
						28.9	< 0.5	< 1	< 20	
DM4	12:36	32	4.3	S	1.0	29.4	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
				B	3.3	28.6	< 0.5	< 1	< 20	
						28.5	< 0.5	< 1	< 20	

Certified by


  
Approved Signatory : K.M. Ho

Date

4/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 11/08/2011 (a.m.) Test No. : 86  
Tide State : MID-FLOOD Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	17:18	31	3.2	S	1.0	29.6	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	2.2	29.3	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
M2	17:06	32	4.1	S	1.0	29.1	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
				B	3.1	28.7	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	
DM4	17:39	31	4.2	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	3.2	29.1	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

11/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 13/08/2011 (a.m.)

Test No. : 87

Tide State : MID-FLOOD

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:13	30	4.2	S	1.0	29.3	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
				B	3.2	29.0	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
M2	9:00	31	5.8	S	1.0	29.7	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	4.8	29.4	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
DM4	9:31	31	5.6	S	1.0	29.3	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
				B	4.6	28.9	< 0.5	< 1	< 20	
						28.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 13/08/2011 (p.m.) Test No. : 87  
Tide State : MID-EBB Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	13:36	32	3.5	S	1.0	30.4	< 0.5	< 1	< 20	
						30.6	< 0.5	< 1	< 20	
				B	2.5	30.6	< 0.5	< 1	< 20	
						30.6	< 0.5	< 1	< 20	
M2	13:24	32	5.1	S	1.0	30.4	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
				B	4.1	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
DM4	13:56	32	4.3	S	1.0	30.5	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	
				B	3.3	30.5	< 0.5	< 1	< 20	
						30.5	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

13/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 16/08/2011 (a.m.) Test No. : 88  
Tide State : MID-FLOOD Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:44	31	4.2	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	3.2	29.0	< 0.5	< 1	< 20	
						28.9	< 0.5	< 1	< 20	
M2	9:32	31	5.8	S	1.0	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	4.8	29.7	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
DM4	10:03	31	5.4	S	1.0	29.6	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	4.4	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

16/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 16/08/2011 (p.m.) Test No. : 88  
Tide State : MID-EBB Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	15:19	33	3.3	S	1.0	30.9	< 0.5	< 1	< 20	
						30.9	< 0.5	< 1	< 20	
				B	2.3	30.7	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	
M2	15:05	33	5.4	S	1.0	31.6	< 0.5	< 1	< 20	
						31.6	< 0.5	< 1	< 20	
				B	4.4	30.9	< 0.5	< 1	< 20	
						30.9	< 0.5	< 1	< 20	
DM4	15:40	33	4.5	S	1.0	29.0	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
				B	3.5	29.0	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	

Certified by



Approved Signatory : K.M. Ho

Date

19/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 18/08/2011 (a.m.)

Test No. : 89

Tide State : MID-FLOOD

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:33	33	4.0	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	3.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
M2	10:21	32	5.4	S	1.0	29.6	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	4.4	29.0	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
DM4	10:51	32	5.0	S	1.0	29.1	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
				B	4.0	28.9	< 0.5	< 1	< 20	
						28.9	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

18/8/2011

**FUGRO TECHNICAL SERVICES LIMITED**

Materialab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materialab.com.hk

**Materialab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**


Date : 18/08/2011 (p.m.) Test No. : 89

Tide State : MID-EBB Weather : FINE

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:11	32	3.4	S	1.0	30.4	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
				B	2.4	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
M2	15:57	32	5.3	S	1.0	30.2	< 0.5	< 1	< 20	
						30.3	< 0.5	< 1	< 20	
				B	4.3	29.8	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
DM4	16:29	32	4.3	S	1.0	30.1	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	3.3	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	

Certified by :


  
Approved Signatory : K.M. Ho

Date :

19/8/2011



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 20/08/2011 (a.m.) Test No. : 90  
Tide State : MID-FLOOD Weather : SUNNY  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	11:30	33	3.9	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	2.9	29.0	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
M2	11:15	33	4.9	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	3.9	29.5	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
DM4	11:55	33	3.6	S	1.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	2.6	29.2	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 20/08/2011 (p.m.)

Test No. : 90


Tide State : MID-EBB

Weather : SUNNY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:46	32.5	3.4	S	1.0	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	2.4	29.4	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
M2	17:01	32.5	4.6	S	1.0	31.1	< 0.5	< 1	< 20	
						31.0	< 0.5	< 1	< 20	
				B	3.6	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
DM4	16:15	32.5	3.3	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	2.3	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 23/08/2011 (a.m.) Test No. : 91  
Tide State : MID-EBB Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:38	30	3.3	S	1.0	29.7	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	2.3	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
M2	9:25	30	5.1	S	1.0	29.9	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	4.1	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
DM4	9:59	30	4.3	S	1.0	29.4	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
				B	3.3	29.6	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

1/9/2011

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.materiallab.com.hk

**MaterialLab**

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

**Field Data Record (Marine Water) - Testing of Cd, Cr and Al**

Date : 23/08/2011 (p.m.) Test No. : 91  
Tide State : MID-FLOOD Weather : FINE  
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	15:51	33	3.3	S	1.0	30.9	< 0.5	< 1	< 20	
						31.0	< 0.5	< 1	< 20	
				B	2.3	30.4	< 0.5	< 1	< 20	
30.4	< 0.5	< 1	< 20							
M2	15:37	33	5.2	S	1.0	30.9	< 0.5	< 1	< 20	
						30.9	< 0.5	< 1	< 20	
				B	4.2	29.0	< 0.5	< 1	< 20	
28.9	< 0.5	< 1	< 20							
DM4	16:09	33	4.6	S	1.0	30.7	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	
				B	3.6	30.7	< 0.5	< 1	< 20	
30.7	< 0.5	< 1	< 20							

Certified by :

  
Approved Signatory : K.M. Ho

Date :

1/9/2011

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1117289
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 26-JUL-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 04-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H016914-H016915				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1117289 supersedes any previous reports with this reference. The completion date of analysis is 26-JUL-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1117289 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics

#### ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**  
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong  
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	26-JUL-2011 10:55	HK1117289-001	<0.5	<1	<20			
M1-S-E-2	26-JUL-2011 10:55	HK1117289-002	<0.5	<1	<20			
M1-B-E-1	26-JUL-2011 10:55	HK1117289-003	<0.5	<1	<20			
M1-B-E-2	26-JUL-2011 10:55	HK1117289-004	<0.5	<1	<20			
M2-S-E-1	26-JUL-2011 10:41	HK1117289-005	<0.5	<1	<20			
M2-S-E-2	26-JUL-2011 10:41	HK1117289-006	<0.5	<1	<20			
M2-B-E-1	26-JUL-2011 10:41	HK1117289-007	<0.5	<1	<20			
M2-B-E-2	26-JUL-2011 10:41	HK1117289-008	<0.5	<1	<20			
DM4-S-E-1	26-JUL-2011 11:13	HK1117289-009	<0.5	<1	<20			
DM4-S-E-2	26-JUL-2011 11:13	HK1117289-010	<0.5	<1	<20			
DM4-B-E-1	26-JUL-2011 11:13	HK1117289-011	<0.5	<1	<20			
DM4-B-E-2	26-JUL-2011 11:13	HK1117289-012	<0.5	<1	<20			
M1-S-F-1	26-JUL-2011 17:05	HK1117289-013	<0.5	<1	<20			
M1-S-F-2	26-JUL-2011 17:05	HK1117289-014	<0.5	<1	<20			
M1-B-F-1	26-JUL-2011 17:05	HK1117289-015	<0.5	<1	<20			
M1-B-F-2	26-JUL-2011 17:05	HK1117289-016	<0.5	<1	<20			
M2-S-F-1	26-JUL-2011 16:52	HK1117289-017	<0.5	<1	<20			
M2-S-F-2	26-JUL-2011 16:52	HK1117289-018	<0.5	<1	<20			
M2-B-F-1	26-JUL-2011 16:52	HK1117289-019	<0.5	<1	<20			
M2-B-F-2	26-JUL-2011 16:52	HK1117289-020	<0.5	<1	<20			
DM4-S-F-1	26-JUL-2011 17:26	HK1117289-021	<0.5	<1	<20			
DM4-S-F-2	26-JUL-2011 17:26	HK1117289-022	<0.5	<1	<20			
DM4-B-F-1	26-JUL-2011 17:26	HK1117289-023	<0.5	<1	<20			
DM4-B-F-2	26-JUL-2011 17:26	HK1117289-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1889415)</b>								
HK1117289-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1117289-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1889416)</b>								
HK1117289-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1117289-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1889417)</b>								
HK1117289-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1889418)</b>								
HK1117289-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER		Method Blank (MB) Report				Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889415)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	104	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	103	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889416)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	107	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889417)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	87.7	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	94.6	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889418)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	94.3	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889415)</b>										
HK1117289-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	97.7	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	95.4	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889416)</b>										
HK1117289-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	81.0	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)													
				Spike		Recovery Limits (%)															
				Concentration	Spike Recovery (%)	Low	High														
Client sample ID				Method: Compound		CAS Number		MS	MSD	Low	High	Value	Control Limit								
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889417)</b>																					
HK1117289-021		DM4-S-F-1		EG020: Cadmium		7440-43-9		10 µg/L		100		----		75		125		----		----	
				EG020: Chromium		7440-47-3		10 µg/L		96.5		----		75		125		----		----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1889418)</b>																					
HK1117289-021		DM4-S-F-1		EG020: Aluminium		7429-90-5		10 µg/L		90.9		----		75		125		----		----	



### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 3  
**Work Order** : HK1117605

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016916  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 28-JUL-2011  
**Date of issue** : 08-AUG-2011  
**No. of samples** - *Received* : 12  
- *Analysed* : 12

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1117605 supersedes any previous reports with this reference. The completion date of analysis is 04-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1117605 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics



### Analytical Results

Sub-Matrix: SEAWATER

Client sample ID	Client sampling date / time	Laboratory sample ID	Compound	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			LOR Unit	0.5 µg/L	1 µg/L	20 µg/L		
			EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	28-JUL-2011 12:18	HK1117605-001		<0.5	<1	<20		
M1-S-E-2	28-JUL-2011 12:18	HK1117605-002		<0.5	<1	<20		
M1-B-E-1	28-JUL-2011 12:18	HK1117605-003		<0.5	<1	<20		
M1-B-E-2	28-JUL-2011 12:18	HK1117605-004		<0.5	<1	<20		
M2-S-E-1	28-JUL-2011 12:06	HK1117605-005		<0.5	<1	<20		
M2-S-E-2	28-JUL-2011 12:06	HK1117605-006		<0.5	<1	<20		
M2-B-E-1	28-JUL-2011 12:06	HK1117605-007		<0.5	<1	<20		
M2-B-E-2	28-JUL-2011 12:06	HK1117605-008		<0.5	<1	<20		
DM4-S-E-1	28-JUL-2011 12:37	HK1117605-009		<0.5	<1	<20		
DM4-S-E-2	28-JUL-2011 12:37	HK1117605-010		<0.5	<1	<20		
DM4-B-E-1	28-JUL-2011 12:37	HK1117605-011		<0.5	<1	<20		
DM4-B-E-2	28-JUL-2011 12:37	HK1117605-012		<0.5	<1	<20		



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894756)</b>								
HK1117605-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1117605-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894757)</b>								
HK1117605-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1117605-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894756)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	97.4	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	96.6	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894757)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	103	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894756)</b>										
HK1117605-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	102	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	101	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1894757)</b>										
HK1117605-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	103	----	75	125	----	----

### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 4  
**Work Order** : HK1117794

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016917-H016918  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 30-JUL-2011  
**Date of issue** : 09-AUG-2011  
**No. of samples** - *Received* : 24  
- *Analysed* : 24

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1117794 supersedes any previous reports with this reference. The completion date of analysis is 04-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1117794 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	30-JUL-2011 09:05	HK1117794-001	<0.5	<1	<20			
M1-S-F-2	30-JUL-2011 09:05	HK1117794-002	<0.5	<1	<20			
M1-B-F-1	30-JUL-2011 09:05	HK1117794-003	<0.5	<1	<20			
M1-B-F-2	30-JUL-2011 09:05	HK1117794-004	<0.5	<1	<20			
M2-S-F-1	30-JUL-2011 08:53	HK1117794-005	<0.5	<1	<20			
M2-S-F-2	30-JUL-2011 08:53	HK1117794-006	<0.5	<1	<20			
M2-B-F-1	30-JUL-2011 08:53	HK1117794-007	<0.5	<1	<20			
M2-B-F-2	30-JUL-2011 08:53	HK1117794-008	<0.5	<1	<20			
DM4-S-F-1	30-JUL-2011 09:25	HK1117794-009	<0.5	<1	<20			
DM4-S-F-2	30-JUL-2011 09:25	HK1117794-010	<0.5	<1	<20			
DM4-B-F-1	30-JUL-2011 09:25	HK1117794-011	<0.5	<1	<20			
DM4-B-F-2	30-JUL-2011 09:25	HK1117794-012	<0.5	<1	<20			
M1-S-E-1	30-JUL-2011 13:20	HK1117794-013	<0.5	<1	<20			
M1-S-E-2	30-JUL-2011 13:20	HK1117794-014	<0.5	<1	<20			
M1-B-E-1	30-JUL-2011 13:20	HK1117794-015	<0.5	<1	<20			
M1-B-E-2	30-JUL-2011 13:20	HK1117794-016	<0.5	<1	<20			
M2-S-E-1	30-JUL-2011 13:07	HK1117794-017	<0.5	<1	<20			
M2-S-E-2	30-JUL-2011 13:07	HK1117794-018	<0.5	<1	<20			
M2-B-E-1	30-JUL-2011 13:07	HK1117794-019	<0.5	<1	<20			
M2-B-E-2	30-JUL-2011 13:07	HK1117794-020	<0.5	<1	<20			
DM4-S-E-1	30-JUL-2011 13:40	HK1117794-021	<0.5	<1	<20			
DM4-S-E-2	30-JUL-2011 13:40	HK1117794-022	<0.5	<1	<20			
DM4-B-E-1	30-JUL-2011 13:40	HK1117794-023	<0.5	<1	<20			
DM4-B-E-2	30-JUL-2011 13:40	HK1117794-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report					
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1898328)</b>									
HK1117794-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
HK1117794-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1898329)</b>									
HK1117794-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
HK1117794-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1898330)</b>									
HK1117794-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1898331)</b>									
HK1117794-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)		
						LCS	DCS	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898328)</b>												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	100	----	85	115	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	101	----	85	115	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898329)</b>												
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	105	----	85	115	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898330)</b>												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	102	----	85	115	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	97.0	----	85	115	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898331)</b>												
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	103	----	85	115	----	----	

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898328)</b>										
HK1117794-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	97.3	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	101	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898329)</b>										
HK1117794-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	98.3	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Client sample ID				Method: Compound				CAS Number				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report							
																Spike		Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
																Concentration	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898330)</b>																							
HK1117794-021		DM4-S-E-1		EG020: Cadmium		7440-43-9		10 µg/L		102		----		75		125		----		----			
				EG020: Chromium		7440-47-3		10 µg/L		102		----		75		125		----		----			
<b>EG: Metals and Major Cations - Filtered (QCLot: 1898331)</b>																							
HK1117794-021		DM4-S-E-1		EG020: Aluminium		7429-90-5		10 µg/L		98.5		----		75		125		----		----			

### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 4  
**Work Order** : HK1118024

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016919-H016920  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 02-AUG-2011  
**Date of issue** : 11-AUG-2011  
**No. of samples** - *Received* : 24  
- *Analysed* : 24

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1118024 supersedes any previous reports with this reference. The completion date of analysis is 04-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1118024 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics





### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	02-AUG-2011 09:17	HK1118024-001	<0.5	<1	<20			
M1-S-F-2	02-AUG-2011 09:17	HK1118024-002	<0.5	<1	<20			
M1-B-F-1	02-AUG-2011 09:17	HK1118024-003	<0.5	<1	<20			
M1-B-F-2	02-AUG-2011 09:17	HK1118024-004	<0.5	<1	<20			
M2-S-F-1	02-AUG-2011 09:04	HK1118024-005	<0.5	<1	<20			
M2-S-F-2	02-AUG-2011 09:04	HK1118024-006	<0.5	<1	<20			
M2-B-F-1	02-AUG-2011 09:04	HK1118024-007	<0.5	<1	<20			
M2-B-F-2	02-AUG-2011 09:04	HK1118024-008	<0.5	<1	<20			
DM4-S-F-1	02-AUG-2011 09:38	HK1118024-009	<0.5	<1	<20			
DM4-S-F-2	02-AUG-2011 09:38	HK1118024-010	<0.5	<1	<20			
DM4-B-F-1	02-AUG-2011 09:38	HK1118024-011	<0.5	<1	<20			
DM4-B-F-2	02-AUG-2011 09:38	HK1118024-012	<0.5	<1	<20			
M1-S-E-1	02-AUG-2011 15:34	HK1118024-013	<0.5	<1	<20			
M1-S-E-2	02-AUG-2011 15:34	HK1118024-014	<0.5	<1	<20			
M1-B-E-1	02-AUG-2011 15:34	HK1118024-015	<0.5	<1	<20			
M1-B-E-2	02-AUG-2011 15:34	HK1118024-016	<0.5	<1	<20			
M2-S-E-1	02-AUG-2011 15:20	HK1118024-017	<0.5	<1	<20			
M2-S-E-2	02-AUG-2011 15:20	HK1118024-018	<0.5	<1	<20			
M2-B-E-1	02-AUG-2011 15:20	HK1118024-019	<0.5	<1	<20			
M2-B-E-2	02-AUG-2011 15:20	HK1118024-020	<0.5	<1	<20			
DM4-S-E-1	02-AUG-2011 15:53	HK1118024-021	<0.5	<1	<20			
DM4-S-E-2	02-AUG-2011 15:53	HK1118024-022	<0.5	<1	<20			
DM4-B-E-1	02-AUG-2011 15:53	HK1118024-023	<0.5	<1	<20			
DM4-B-E-2	02-AUG-2011 15:53	HK1118024-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report					
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1900056)</b>									
HK1118024-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
HK1118024-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1900057)</b>									
HK1118024-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
HK1118024-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1900058)</b>									
HK1118024-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1900059)</b>									
HK1118024-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report				Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)			
						LCS	DCS	Low	High	Value	Control Limit		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900056)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	104	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	101	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900057)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	101	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900058)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	93.6	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	100	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900059)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	102	----	85	115	----	----		

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900056)</b>										
HK1118024-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	97.3	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	103	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900057)</b>										
HK1118024-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	95.2	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)				
				Spike		Recovery Limits (%)						
				Concentration	Spike Recovery (%)	Low	High					
Method: Compound				CAS Number	MS	MSD	Low	High	Value	Control Limit		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900058)</b>												
HK1118024-021		DM4-S-E-1		EG020: Cadmium	7440-43-9	10 µg/L	92.4	----	75	125	----	----
				EG020: Chromium	7440-47-3	10 µg/L	93.2	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1900059)</b>												
HK1118024-021		DM4-S-E-1		EG020: Aluminium	7429-90-5	10 µg/L	104	----	75	125	----	----

### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 4  
**Work Order** : HK1118246

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016921-H016922  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 04-AUG-2011  
**Date of issue** : 15-AUG-2011  
**No. of samples** - *Received* : 24  
- *Analysed* : 24

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1118246 supersedes any previous reports with this reference. The completion date of analysis is 10-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1118246 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics



### Analytical Results

Sub-Matrix: SEAWATER

Client sample ID	Client sampling date / time	Laboratory sample ID	Compound	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			LOR Unit	0.5 µg/L	1 µg/L	20 µg/L		
			EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	04-AUG-2011 10:50	HK1118246-001	<0.5	<1	<20			
M1-S-F-2	04-AUG-2011 10:50	HK1118246-002	<0.5	<1	<20			
M1-B-F-1	04-AUG-2011 10:50	HK1118246-003	<0.5	<1	<20			
M1-B-F-2	04-AUG-2011 10:50	HK1118246-004	<0.5	<1	<20			
M2-S-F-1	04-AUG-2011 10:36	HK1118246-005	<0.5	<1	<20			
M2-S-F-2	04-AUG-2011 10:36	HK1118246-006	<0.5	<1	<20			
M2-B-F-1	04-AUG-2011 10:36	HK1118246-007	<0.5	<1	<20			
M2-B-F-2	04-AUG-2011 10:36	HK1118246-008	<0.5	<1	<20			
DM4-S-F-1	04-AUG-2011 11:10	HK1118246-009	<0.5	<1	<20			
DM4-S-F-2	04-AUG-2011 11:10	HK1118246-010	<0.5	<1	<20			
DM4-B-F-1	04-AUG-2011 11:10	HK1118246-011	<0.5	<1	<20			
DM4-B-F-2	04-AUG-2011 11:10	HK1118246-012	<0.5	<1	<20			
M1-S-E-1	04-AUG-2011 16:46	HK1118246-013	<0.5	<1	<20			
M1-S-E-2	04-AUG-2011 16:46	HK1118246-014	<0.5	<1	<20			
M1-B-E-1	04-AUG-2011 16:46	HK1118246-015	<0.5	<1	<20			
M1-B-E-2	04-AUG-2011 16:46	HK1118246-016	<0.5	<1	<20			
M2-S-E-1	04-AUG-2011 16:33	HK1118246-017	<0.5	<1	<20			
M2-S-E-2	04-AUG-2011 16:33	HK1118246-018	<0.5	<1	<20			
M2-B-E-1	04-AUG-2011 16:33	HK1118246-019	<0.5	<1	<20			
M2-B-E-2	04-AUG-2011 16:33	HK1118246-020	<0.5	<1	<20			
DM4-S-E-1	04-AUG-2011 17:07	HK1118246-021	<0.5	<1	<20			
DM4-S-E-2	04-AUG-2011 17:07	HK1118246-022	<0.5	<1	<20			
DM4-B-E-1	04-AUG-2011 17:07	HK1118246-023	<0.5	<1	<20			
DM4-B-E-2	04-AUG-2011 17:07	HK1118246-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903874)</b>								
HK1118246-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1118246-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903875)</b>								
HK1118246-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1118246-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903876)</b>								
HK1118246-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903877)</b>								
HK1118246-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903874)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	97.8	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	99.1	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903875)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	102	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903876)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	104	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	109	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903877)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	106	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903874)</b>										
HK1118246-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	102	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	108	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1903875)</b>										
HK1118246-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	90.7	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Client sample ID				Method: Compound				CAS Number				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report							
																Spike		Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
																Concentration	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1903876)</b>																							
HK1118246-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----													
		EG020: Chromium	7440-47-3	10 µg/L	105	----	75	125	----	----													
<b>EG: Metals and Major Cations - Filtered (QCLot: 1903877)</b>																							
HK1118246-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	102	----	75	125	----	----													

### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 4  
**Work Order** : HK1118442

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016923-H016924  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 06-AUG-2011  
**Date of issue** : 16-AUG-2011  
**No. of samples** - *Received* : 24  
- *Analysed* : 24

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1118442 supersedes any previous reports with this reference. The completion date of analysis is 10-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1118442 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics





### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	06-AUG-2011 11:57	HK1118442-001	<0.5	<1	<20			
M1-S-F-2	06-AUG-2011 11:57	HK1118442-002	<0.5	<1	<20			
M1-B-F-1	06-AUG-2011 11:57	HK1118442-003	<0.5	<1	<20			
M1-B-F-2	06-AUG-2011 11:57	HK1118442-004	<0.5	<1	<20			
M2-S-F-1	06-AUG-2011 11:44	HK1118442-005	<0.5	<1	<20			
M2-S-F-2	06-AUG-2011 11:44	HK1118442-006	<0.5	<1	<20			
M2-B-F-1	06-AUG-2011 11:44	HK1118442-007	<0.5	<1	<20			
M2-B-F-2	06-AUG-2011 11:44	HK1118442-008	<0.5	<1	<20			
DM4-S-F-1	06-AUG-2011 12:16	HK1118442-009	<0.5	<1	<20			
DM4-S-F-2	06-AUG-2011 12:16	HK1118442-010	<0.5	<1	<20			
DM4-B-F-1	06-AUG-2011 12:16	HK1118442-011	<0.5	<1	<20			
DM4-B-F-2	06-AUG-2011 12:16	HK1118442-012	<0.5	<1	<20			
M1-S-E-1	06-AUG-2011 16:53	HK1118442-013	<0.5	<1	<20			
M1-S-E-2	06-AUG-2011 16:53	HK1118442-014	<0.5	<1	<20			
M1-B-E-1	06-AUG-2011 16:53	HK1118442-015	<0.5	<1	<20			
M1-B-E-2	06-AUG-2011 16:53	HK1118442-016	<0.5	<1	<20			
M2-S-E-1	06-AUG-2011 16:41	HK1118442-017	<0.5	<1	<20			
M2-S-E-2	06-AUG-2011 16:41	HK1118442-018	<0.5	<1	<20			
M2-B-E-1	06-AUG-2011 16:41	HK1118442-019	<0.5	<1	<20			
M2-B-E-2	06-AUG-2011 16:41	HK1118442-020	<0.5	<1	<20			
DM4-S-E-1	06-AUG-2011 17:12	HK1118442-021	<0.5	<1	<20			
DM4-S-E-2	06-AUG-2011 17:12	HK1118442-022	<0.5	<1	<20			
DM4-B-E-1	06-AUG-2011 17:12	HK1118442-023	<0.5	<1	<20			
DM4-B-E-2	06-AUG-2011 17:12	HK1118442-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report					
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1906849)</b>									
HK1118442-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
HK1118442-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1906850)</b>									
HK1118442-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
HK1118442-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1906851)</b>									
HK1118442-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1906852)</b>									
HK1118442-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906849)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	91.5	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	91.0	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906850)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	88.2	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906851)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	101	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	103	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906852)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	114	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906849)</b>										
HK1118442-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	106	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	108	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906850)</b>										
HK1118442-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	112	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike		Recovery Limits (%)					
				Concentration	Spike Recovery (%)	Low	High				
Method: Compound				CAS Number	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906851)</b>											
HK1118442-021		DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	98.7	----	75	125	----	----
			EG020: Chromium	7440-47-3	10 µg/L	98.0	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1906852)</b>											
HK1118442-021		DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	98.9	----	75	125	----	----

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1118694
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 09-AUG-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 18-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H016925-H016926				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1118694 supersedes any previous reports with this reference. The completion date of analysis is 15-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1118694 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics

#### ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**  
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong  
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	09-AUG-2011 10:38	HK1118694-001	<0.5	<1	<20			
M1-S-E-2	09-AUG-2011 10:38	HK1118694-002	<0.5	<1	<20			
M1-B-E-1	09-AUG-2011 10:38	HK1118694-003	<0.5	<1	<20			
M1-B-E-2	09-AUG-2011 10:38	HK1118694-004	<0.5	<1	<20			
M2-S-E-1	09-AUG-2011 10:23	HK1118694-005	<0.5	<1	<20			
M2-S-E-2	09-AUG-2011 10:23	HK1118694-006	<0.5	<1	<20			
M2-B-E-1	09-AUG-2011 10:23	HK1118694-007	<0.5	<1	<20			
M2-B-E-2	09-AUG-2011 10:23	HK1118694-008	<0.5	<1	<20			
DM4-S-E-1	09-AUG-2011 10:56	HK1118694-009	<0.5	<1	<20			
DM4-S-E-2	09-AUG-2011 10:56	HK1118694-010	<0.5	<1	<20			
DM4-B-E-1	09-AUG-2011 10:56	HK1118694-011	<0.5	<1	<20			
DM4-B-E-2	09-AUG-2011 10:56	HK1118694-012	<0.5	<1	<20			
M1-S-F-1	09-AUG-2011 17:12	HK1118694-013	<0.5	<1	<20			
M1-S-F-2	09-AUG-2011 17:12	HK1118694-014	<0.5	<1	<20			
M1-B-F-1	09-AUG-2011 17:12	HK1118694-015	<0.5	<1	<20			
M1-B-F-2	09-AUG-2011 17:12	HK1118694-016	<0.5	<1	<20			
M2-S-F-1	09-AUG-2011 17:00	HK1118694-017	<0.5	<1	<20			
M2-S-F-2	09-AUG-2011 17:00	HK1118694-018	<0.5	<1	<20			
M2-B-F-1	09-AUG-2011 17:00	HK1118694-019	<0.5	<1	<20			
M2-B-F-2	09-AUG-2011 17:00	HK1118694-020	<0.5	<1	<20			
DM4-S-F-1	09-AUG-2011 17:31	HK1118694-021	<0.5	<1	<20			
DM4-S-F-2	09-AUG-2011 17:31	HK1118694-022	<0.5	<1	<20			
DM4-B-F-1	09-AUG-2011 17:31	HK1118694-023	<0.5	<1	<20			
DM4-B-F-2	09-AUG-2011 17:31	HK1118694-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1909648)</b>								
HK1118694-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1118694-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1909649)</b>								
HK1118694-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1118694-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1909650)</b>								
HK1118694-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1909651)</b>								
HK1118694-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report				Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)			
						LCS	DCS	Low	High	Value	Control Limit		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909648)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	98.1	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	95.4	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909649)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	103	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909650)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	94.9	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	95.3	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909651)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	103	----	85	115	----	----		

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909648)</b>										
HK1118694-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	90.2	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	88.2	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909649)</b>										
HK1118694-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	79.5	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike		Recovery Limits (%)				Control Limit	
				Concentration	Spike Recovery (%)	Low	High			Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909650)</b>											
HK1118694-021	DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----	
		EG020: Chromium	7440-47-3	10 µg/L	100	----	75	125	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1909651)</b>											
HK1118694-021	DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	108	----	75	125	----	----	

### CERTIFICATE OF ANALYSIS

**Client** : FUGRO TECHNICAL SERVICES LIMITED  
**Contact** : MR JOHN HO  
**Address** : MATERIAL DIVISION  
FUGRO DEVELOPMENT CENTRE,  
NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK  
ROAD,  
TAI LAM, TUEN MUN, N.T., HONG KONG

**Laboratory** : ALS Technichem HK Pty Ltd  
**Contact** : Chan Kwok Fai, Godfrey  
**Address** : 11/F., Chung Shun Knitting Centre, 1 - 3 Wing  
Yip Street, Kwai Chung, N.T., Hong Kong

**Page** : 1 of 4  
**Work Order** : HK1118933

**E-mail** : jho@fugro.com.hk  
**Telephone** : +852 2452 7142  
**Facsimile** : +852 2450 6138  
**Project** : ----  
**Order number** : ----  
**C-O-C number** : H016927-H016928  
**Site** : ----

**E-mail** : Godfrey.Chan@alsglobal.com  
**Telephone** : +852 2610 1044  
**Facsimile** : +852 2610 2021  
**Quote number** : ----

**Date received** : 11-AUG-2011  
**Date of issue** : 22-AUG-2011  
**No. of samples** - *Received* : 24  
- *Analysed* : 24

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1118933 supersedes any previous reports with this reference. The completion date of analysis is 22-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1118933 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics





### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	11-AUG-2011 12:14	HK1118933-001	<0.5	<1	<20			
M1-S-E-2	11-AUG-2011 12:14	HK1118933-002	<0.5	<1	<20			
M1-B-E-1	11-AUG-2011 12:14	HK1118933-003	<0.5	<1	<20			
M1-B-E-2	11-AUG-2011 12:14	HK1118933-004	<0.5	<1	<20			
M2-S-E-1	11-AUG-2011 12:00	HK1118933-005	<0.5	<1	<20			
M2-S-E-2	11-AUG-2011 12:00	HK1118933-006	<0.5	----	<20			
M2-B-E-1	11-AUG-2011 12:00	HK1118933-007	<0.5	<1	<20			
M2-B-E-2	11-AUG-2011 12:00	HK1118933-008	<0.5	<1	<20			
DM4-S-E-1	11-AUG-2011 12:36	HK1118933-009	<0.5	<1	<20			
DM4-S-E-2	11-AUG-2011 12:36	HK1118933-010	<0.5	<1	<20			
DM4-B-E-1	11-AUG-2011 12:36	HK1118933-011	<0.5	<1	<20			
DM4-B-E-2	11-AUG-2011 12:36	HK1118933-012	<0.5	<1	<20			
M1-S-F-1	11-AUG-2011 17:18	HK1118933-013	<0.5	<1	<20			
M1-S-F-2	11-AUG-2011 17:18	HK1118933-014	<0.5	<1	<20			
M1-B-F-1	11-AUG-2011 17:18	HK1118933-015	<0.5	<1	<20			
M1-B-F-2	11-AUG-2011 17:18	HK1118933-016	<0.5	<1	<20			
M2-S-F-1	11-AUG-2011 17:06	HK1118933-017	<0.5	<1	<20			
M2-S-F-2	11-AUG-2011 17:06	HK1118933-018	<0.5	<1	<20			
M2-B-F-1	11-AUG-2011 17:06	HK1118933-019	<0.5	<1	<20			
M2-B-F-2	11-AUG-2011 17:06	HK1118933-020	<0.5	<1	<20			
DM4-S-F-1	11-AUG-2011 17:39	HK1118933-021	<0.5	<1	<20			
DM4-S-F-2	11-AUG-2011 17:39	HK1118933-022	<0.5	<1	<20			
DM4-B-F-1	11-AUG-2011 17:39	HK1118933-023	<0.5	<1	<20			
DM4-B-F-2	11-AUG-2011 17:39	HK1118933-024	<0.5	<1	<20			

### Analytical Results

Sub-Matrix: SEAWATER		
Method: Compound	Client sample ID - Client sampling date / time	Analytical Results
<b>EG: Metals and Major Cations - Filtered</b>		
EG020 F A: Chromium	M2-S-E-2 - 11-AUG-2011 12:00	<1



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report					
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1913395)</b>									
HK1118933-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
HK1118933-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1913396)</b>									
HK1118933-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
HK1118933-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1913397)</b>									
HK1118933-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0	
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0	
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1913398)</b>									
HK1118933-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0	

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report				Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)			
						LCS	DCS	Low	High	Value	Control Limit		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913395)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	85.2	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	87.2	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913396)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	108	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913397)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	90.1	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	91.7	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913398)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	106	----	85	115	----	----		

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913395)</b>										
HK1118933-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	95.5	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	98.4	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913396)</b>										
HK1118933-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	109	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike		Recovery Limits (%)				RPDs (%)	
				Concentration	Spike Recovery (%)	Low	High			Value	Control Limit
Method: Compound				CAS Number	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913397)</b>											
HK1118933-021		DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	100	----	75	125	----	----
			EG020: Chromium	7440-47-3	10 µg/L	107	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1913398)</b>											
HK1118933-021		DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	119	----	75	125	----	----

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1119107
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 13-AUG-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 22-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H016929-H016930				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1119107 supersedes any previous reports with this reference. The completion date of analysis is 22-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1119107 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	13-AUG-2011 13:36	HK1119107-001	<0.5	<1	<20			
M1-S-E-2	13-AUG-2011 13:36	HK1119107-002	<0.5	<1	<20			
M1-B-E-1	13-AUG-2011 13:36	HK1119107-003	<0.5	<1	<20			
M1-B-E-2	13-AUG-2011 13:36	HK1119107-004	<0.5	<1	<20			
M2-S-E-1	13-AUG-2011 13:24	HK1119107-005	<0.5	<1	<20			
M2-S-E-2	13-AUG-2011 13:24	HK1119107-006	<0.5	<1	<20			
M2-B-E-1	13-AUG-2011 13:24	HK1119107-007	<0.5	<1	<20			
M2-B-E-2	13-AUG-2011 13:24	HK1119107-008	<0.5	<1	<20			
DM4-S-E-1	13-AUG-2011 13:56	HK1119107-009	<0.5	<1	<20			
DM4-S-E-2	13-AUG-2011 13:56	HK1119107-010	<0.5	<1	<20			
DM4-B-E-1	13-AUG-2011 13:56	HK1119107-011	<0.5	<1	<20			
DM4-B-E-2	13-AUG-2011 13:56	HK1119107-012	<0.5	<1	<20			
M1-S-F-1	13-AUG-2011 09:13	HK1119107-013	<0.5	<1	<20			
M1-S-F-2	13-AUG-2011 09:13	HK1119107-014	<0.5	<1	<20			
M1-B-F-1	13-AUG-2011 09:13	HK1119107-015	<0.5	<1	<20			
M1-B-F-2	13-AUG-2011 09:13	HK1119107-016	<0.5	<1	<20			
M2-S-F-1	13-AUG-2011 09:00	HK1119107-017	<0.5	<1	<20			
M2-S-F-2	13-AUG-2011 09:00	HK1119107-018	<0.5	<1	<20			
M2-B-F-1	13-AUG-2011 09:00	HK1119107-019	<0.5	<1	<20			
M2-B-F-2	13-AUG-2011 09:00	HK1119107-020	<0.5	<1	<20			
DM4-S-F-1	13-AUG-2011 09:31	HK1119107-021	<0.5	<1	<20			
DM4-S-F-2	13-AUG-2011 09:31	HK1119107-022	<0.5	<1	<20			
DM4-B-F-1	13-AUG-2011 09:31	HK1119107-023	<0.5	<1	<20			
DM4-B-F-2	13-AUG-2011 09:31	HK1119107-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1914304)</b>								
HK1119107-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1119107-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1914305)</b>								
HK1119107-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1119107-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1914306)</b>								
HK1119107-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1914307)</b>								
HK1119107-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914304)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	98.3	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	97.3	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914305)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	101	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914306)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	95.5	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	98.2	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914307)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	96.4	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914304)</b>										
HK1119107-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	98.6	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	98.5	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914305)</b>										
HK1119107-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	113	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike		Recovery Limits (%)					
				Concentration	Spike Recovery (%)	Low	High				
Client sample ID				Method: Compound		CAS Number		Value		Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914306)</b>											
HK1119107-021	DM4-S-F-1	EG020: Cadmium		7440-43-9	10 µg/L	98.9	----	75	125	----	----
		EG020: Chromium		7440-47-3	10 µg/L	108	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1914307)</b>											
HK1119107-021	DM4-S-F-1	EG020: Aluminium		7429-90-5	10 µg/L	122	----	75	125	----	----

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1119239
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 16-AUG-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 24-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H016931-H016932				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1119239 supersedes any previous reports with this reference. The completion date of analysis is 23-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1119239 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signature</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor	Inorganics





### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	16-AUG-2011 09:44	HK1119239-001	<0.5	<1	<20			
M1-S-F-2	16-AUG-2011 09:44	HK1119239-002	<0.5	<1	<20			
M1-B-F-1	16-AUG-2011 09:44	HK1119239-003	<0.5	<1	<20			
M1-B-F-2	16-AUG-2011 09:44	HK1119239-004	<0.5	<1	<20			
M2-S-F-1	16-AUG-2011 09:32	HK1119239-005	<0.5	<1	<20			
M2-S-F-2	16-AUG-2011 09:32	HK1119239-006	<0.5	<1	<20			
M2-B-F-1	16-AUG-2011 09:32	HK1119239-007	<0.5	<1	<20			
M2-B-F-2	16-AUG-2011 09:32	HK1119239-008	<0.5	<1	<20			
DM4-S-F-1	16-AUG-2011 10:03	HK1119239-009	<0.5	<1	<20			
DM4-S-F-2	16-AUG-2011 10:03	HK1119239-010	<0.5	<1	<20			
DM4-B-F-1	16-AUG-2011 10:03	HK1119239-011	<0.5	<1	<20			
DM4-B-F-2	16-AUG-2011 10:03	HK1119239-012	<0.5	<1	<20			
M1-S-E-1	16-AUG-2011 15:19	HK1119239-013	<0.5	<1	<20			
M1-S-E-2	16-AUG-2011 15:19	HK1119239-014	<0.5	<1	<20			
M1-B-E-1	16-AUG-2011 15:19	HK1119239-015	<0.5	<1	<20			
M1-B-E-2	16-AUG-2011 15:19	HK1119239-016	<0.5	<1	<20			
M2-S-E-1	16-AUG-2011 15:05	HK1119239-017	<0.5	<1	<20			
M2-S-E-2	16-AUG-2011 15:05	HK1119239-018	<0.5	<1	<20			
M2-B-E-1	16-AUG-2011 15:05	HK1119239-019	<0.5	<1	<20			
M2-B-E-2	16-AUG-2011 15:05	HK1119239-020	<0.5	<1	<20			
DM4-S-E-1	16-AUG-2011 15:40	HK1119239-021	<0.5	<1	<20			
DM4-S-E-2	16-AUG-2011 15:40	HK1119239-022	<0.5	<1	<20			
DM4-B-E-1	16-AUG-2011 15:40	HK1119239-023	<0.5	<1	<20			
DM4-B-E-2	16-AUG-2011 15:40	HK1119239-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920845)</b>								
HK1119239-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1119239-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920846)</b>								
HK1119239-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1119239-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920847)</b>								
HK1119239-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920848)</b>								
HK1119239-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report				Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)			
						LCS	DCS	Low	High	Value	Control Limit		
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920845)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	96.4	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	98.2	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920846)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	96.5	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920847)</b>													
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	101	----	85	115	----	----		
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	102	----	85	115	----	----		
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920848)</b>													
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	101	----	85	115	----	----		

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920845)</b>										
HK1119239-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	98.7	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	107	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1920846)</b>										
HK1119239-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	103	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Client sample ID				Method: Compound				CAS Number				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report							
																Spike		Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
																Concentration	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1920847)</b>																							
HK1119239-021		DM4-S-E-1		EG020: Cadmium		7440-43-9		10 µg/L		101		----		75		125		----		----			
				EG020: Chromium		7440-47-3		10 µg/L		105		----		75		125		----		----			
<b>EG: Metals and Major Cations - Filtered (QCLot: 1920848)</b>																							
HK1119239-021		DM4-S-E-1		EG020: Aluminium		7429-90-5		10 µg/L		97.4		----		75		125		----		----			

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1119515
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 18-AUG-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 29-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H016933-H016934				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1119515 supersedes any previous reports with this reference. The completion date of analysis is 23-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1119515 :  
Sample(s) were received in a chilled condition.  
Water sample(s) analysed and reported on an as received basis.  
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Chan Kwok Fai, Godfrey	Laboratory Manager	Inorganics

#### ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**  
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong  
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	18-AUG-2011 10:33	HK1119515-001	<0.5	<1	<20			
M1-S-F-2	18-AUG-2011 10:33	HK1119515-002	<0.5	<1	<20			
M1-B-F-1	18-AUG-2011 10:33	HK1119515-003	<0.5	<1	<20			
M1-B-F-2	18-AUG-2011 10:33	HK1119515-004	<0.5	<1	<20			
M2-S-F-1	18-AUG-2011 10:21	HK1119515-005	<0.5	<1	<20			
M2-S-F-2	18-AUG-2011 10:21	HK1119515-006	<0.5	<1	<20			
M2-B-F-1	18-AUG-2011 10:21	HK1119515-007	<0.5	<1	<20			
M2-B-F-2	18-AUG-2011 10:21	HK1119515-008	<0.5	<1	<20			
DM4-S-F-1	18-AUG-2011 10:51	HK1119515-009	<0.5	<1	<20			
DM4-S-F-2	18-AUG-2011 10:51	HK1119515-010	<0.5	<1	<20			
DM4-B-F-1	18-AUG-2011 10:51	HK1119515-011	<0.5	<1	<20			
DM4-B-F-2	18-AUG-2011 10:51	HK1119515-012	<0.5	<1	<20			
M1-S-E-1	18-AUG-2011 16:11	HK1119515-013	<0.5	<1	<20			
M1-S-E-2	18-AUG-2011 16:11	HK1119515-014	<0.5	<1	<20			
M1-B-E-1	18-AUG-2011 16:11	HK1119515-015	<0.5	<1	<20			
M1-B-E-2	18-AUG-2011 16:11	HK1119515-016	<0.5	<1	<20			
M2-S-E-1	18-AUG-2011 15:57	HK1119515-017	<0.5	<1	<20			
M2-S-E-2	18-AUG-2011 15:57	HK1119515-018	<0.5	<1	<20			
M2-B-E-1	18-AUG-2011 15:57	HK1119515-019	<0.5	<1	<20			
M2-B-E-2	18-AUG-2011 15:57	HK1119515-020	<0.5	<1	<20			
DM4-S-E-1	18-AUG-2011 16:29	HK1119515-021	<0.5	<1	<20			
DM4-S-E-2	18-AUG-2011 16:29	HK1119515-022	<0.5	<1	<20			
DM4-B-E-1	18-AUG-2011 16:29	HK1119515-023	<0.5	<1	<20			
DM4-B-E-2	18-AUG-2011 16:29	HK1119515-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921619)</b>								
HK1119515-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1119515-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921620)</b>								
HK1119515-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1119515-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921621)</b>								
HK1119515-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921622)</b>								
HK1119515-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921619)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	94.3	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	96.8	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921620)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	97.4	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921621)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	91.7	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	100	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921622)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	106	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921619)</b>										
HK1119515-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	92.1	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	98.9	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1921620)</b>										
HK1119515-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	97.5	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike		Recovery Limits (%)				Value	
				Concentration	Spike Recovery (%)	Low	High			Control Limit	Control Limit
<b>EG: Metals and Major Cations - Filtered (QCLot: 1921621)</b>											
HK1119515-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----	
		EG020: Chromium	7440-47-3	10 µg/L	106	----	75	125	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1921622)</b>											
HK1119515-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	107	----	75	125	----	----	

### CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1119647
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 21-AUG-2011
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 30-AUG-2011
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H020456-H020457				
<i>Site</i>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1119647 supersedes any previous reports with this reference. The completion date of analysis is 24-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1119647:

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Chan Kwok Fai, Godfrey	Laboratory Manager	Inorganics

#### ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**  
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong  
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company





### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	20-AUG-2011 11:30	HK1119647-001	<0.5	<1	<20			
M1-S-F-2	20-AUG-2011 11:30	HK1119647-002	<0.5	<1	<20			
M1-B-F-1	20-AUG-2011 11:30	HK1119647-003	<0.5	<1	<20			
M1-B-F-2	20-AUG-2011 11:30	HK1119647-004	<0.5	<1	<20			
M2-S-F-1	20-AUG-2011 11:15	HK1119647-005	<0.5	<1	<20			
M2-S-F-2	20-AUG-2011 11:15	HK1119647-006	<0.5	<1	<20			
M2-B-F-1	20-AUG-2011 11:15	HK1119647-007	<0.5	<1	<20			
M2-B-F-2	20-AUG-2011 11:15	HK1119647-008	<0.5	<1	<20			
DM4-S-F-1	20-AUG-2011 11:55	HK1119647-009	<0.5	<1	<20			
DM4-S-F-2	20-AUG-2011 11:55	HK1119647-010	<0.5	<1	<20			
DM4-B-F-1	20-AUG-2011 11:55	HK1119647-011	<0.5	<1	<20			
DM4-B-F-2	20-AUG-2011 11:55	HK1119647-012	<0.5	<1	<20			
M1-S-E-1	20-AUG-2011 16:46	HK1119647-013	<0.5	<1	<20			
M1-S-E-2	20-AUG-2011 16:46	HK1119647-014	<0.5	<1	<20			
M1-B-E-1	20-AUG-2011 16:46	HK1119647-015	<0.5	<1	<20			
M1-B-E-2	20-AUG-2011 16:46	HK1119647-016	<0.5	<1	<20			
M2-S-E-1	20-AUG-2011 17:01	HK1119647-017	<0.5	<1	<20			
M2-S-E-2	20-AUG-2011 17:01	HK1119647-018	<0.5	<1	<20			
M2-B-E-1	20-AUG-2011 17:01	HK1119647-019	<0.5	<1	<20			
M2-B-E-2	20-AUG-2011 17:01	HK1119647-020	<0.5	<1	<20			
DM4-S-E-1	20-AUG-2011 16:15	HK1119647-021	<0.5	<1	<20			
DM4-S-E-2	20-AUG-2011 16:15	HK1119647-022	<0.5	<1	<20			
DM4-B-E-1	20-AUG-2011 16:15	HK1119647-023	<0.5	<1	<20			
DM4-B-E-2	20-AUG-2011 16:15	HK1119647-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924314)</b>								
HK1119647-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1119647-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924315)</b>								
HK1119647-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1119647-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924316)</b>								
HK1119647-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924317)</b>								
HK1119647-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924314)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	95.0	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	97.7	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924315)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	107	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924316)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	97.6	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	98.5	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924317)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	112	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924314)</b>										
HK1119647-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	97.0	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	101	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1924315)</b>										
HK1119647-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	92.2	----	75	125	----	----



Matrix: WATER

Laboratory sample ID				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report				RPDs (%)			
				Spike Recovery (%)		Recovery Limits (%)				Value	Control Limit
				MS	MSD	Low	High				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	MS	MSD	Low	High	Value	Control Limit	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1924316)</b>											
HK1119647-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	100	----	75	125	----	----	
		EG020: Chromium	7440-47-3	10 µg/L	102	----	75	125	----	----	
<b>EG: Metals and Major Cations - Filtered (QCLot: 1924317)</b>											
HK1119647-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	106	----	75	125	----	----	

### CERTIFICATE OF ANALYSIS

<b>Client</b>	: FUGRO TECHNICAL SERVICES LIMITED	<b>Laboratory</b>	: ALS Technichem HK Pty Ltd	<b>Page</b>	: 1 of 4
<b>Contact</b>	: MR JOHN HO	<b>Contact</b>	: Chan Kwok Fai, Godfrey	<b>Work Order</b>	: HK1119834
<b>Address</b>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T., HONG KONG	<b>Address</b>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<b>E-mail</b>	: jho@fugro.com.hk	<b>E-mail</b>	: Godfrey.Chan@alsglobal.com	<b>Date received</b>	: 23-AUG-2011
<b>Telephone</b>	: +852 2452 7142	<b>Telephone</b>	: +852 2610 1044	<b>Date of issue</b>	: 01-SEP-2011
<b>Facsimile</b>	: +852 2450 6138	<b>Facsimile</b>	: +852 2610 2021	<b>No. of samples</b>	- Received : 24
<b>Project</b>	: ----	<b>Quote number</b>	: ----		- Analysed : 24
<b>Order number</b>	: ----				
<b>C-O-C number</b>	: H016935-H016936				
<b>Site</b>	: ----				

#### Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1119834 supersedes any previous reports with this reference. The completion date of analysis is 24-AUG-2011. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1119834 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<b>Signatory</b>	<b>Position</b>	<b>Authorised results for:-</b>
Chan Kwok Fai, Godfrey	Laboratory Manager	Inorganics

#### ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**  
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong  
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



### Analytical Results

Sub-Matrix: SEAWATER			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	23-AUG-2011 09:38	HK1119834-001	<0.5	<1	<20			
M1-S-E-2	23-AUG-2011 09:38	HK1119834-002	<0.5	<1	<20			
M1-B-E-1	23-AUG-2011 09:38	HK1119834-003	<0.5	<1	<20			
M1-B-E-2	23-AUG-2011 09:38	HK1119834-004	<0.5	<1	<20			
M2-S-E-1	23-AUG-2011 09:25	HK1119834-005	<0.5	<1	<20			
M2-S-E-2	23-AUG-2011 09:25	HK1119834-006	<0.5	<1	<20			
M2-B-E-1	23-AUG-2011 09:25	HK1119834-007	<0.5	<1	<20			
M2-B-E-2	23-AUG-2011 09:25	HK1119834-008	<0.5	<1	<20			
DM4-S-E-1	23-AUG-2011 09:59	HK1119834-009	<0.5	<1	<20			
DM4-S-E-2	23-AUG-2011 09:59	HK1119834-010	<0.5	<1	<20			
DM4-B-E-1	23-AUG-2011 09:59	HK1119834-011	<0.5	<1	<20			
DM4-B-E-2	23-AUG-2011 09:59	HK1119834-012	<0.5	<1	<20			
M1-S-F-1	23-AUG-2011 15:51	HK1119834-013	<0.5	<1	<20			
M1-S-F-2	23-AUG-2011 15:51	HK1119834-014	<0.5	<1	<20			
M1-B-F-1	23-AUG-2011 15:51	HK1119834-015	<0.5	<1	<20			
M1-B-F-2	23-AUG-2011 15:51	HK1119834-016	<0.5	<1	<20			
M2-S-F-1	23-AUG-2011 15:37	HK1119834-017	<0.5	<1	<20			
M2-S-F-2	23-AUG-2011 15:37	HK1119834-018	<0.5	<1	<20			
M2-B-F-1	23-AUG-2011 15:37	HK1119834-019	<0.5	<1	<20			
M2-B-F-2	23-AUG-2011 15:37	HK1119834-020	<0.5	<1	<20			
DM4-S-F-1	23-AUG-2011 16:09	HK1119834-021	<0.5	<1	<20			
DM4-S-F-2	23-AUG-2011 16:09	HK1119834-022	<0.5	<1	<20			
DM4-B-F-1	23-AUG-2011 16:09	HK1119834-023	<0.5	<1	<20			
DM4-B-F-2	23-AUG-2011 16:09	HK1119834-024	<0.5	<1	<20			



### Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926356)</b>								
HK1119834-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1119834-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926357)</b>								
HK1119834-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1119834-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926358)</b>								
HK1119834-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926359)</b>								
HK1119834-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

### Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926356)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	97.1	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	99.6	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926357)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	96.1	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926358)</b>											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.5	10 µg/L	93.5	----	85	115	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	95.9	----	85	115	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926359)</b>											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	101	----	85	115	----	----

### Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926356)</b>										
HK1119834-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	99.8	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	102	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QC Lot: 1926357)</b>										
HK1119834-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	107	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
				Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number							
<b>EG: Metals and Major Cations - Filtered (QCLot: 1926358)</b>										
HK1119834-021	DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	102	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	104	----	75	125	----	----
<b>EG: Metals and Major Cations - Filtered (QCLot: 1926359)</b>										
HK1119834-021	DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	114	----	75	125	----	----

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 4

#### Graphical Presentation of Monitoring Data




# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W1 - Dissolved Oxygen Content

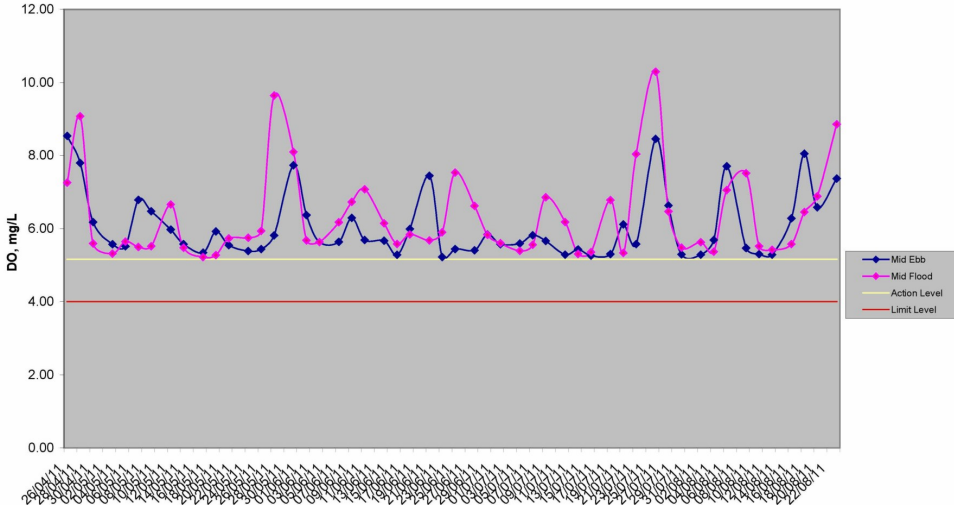


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W1 - Turbidity (Mid-Ebb)

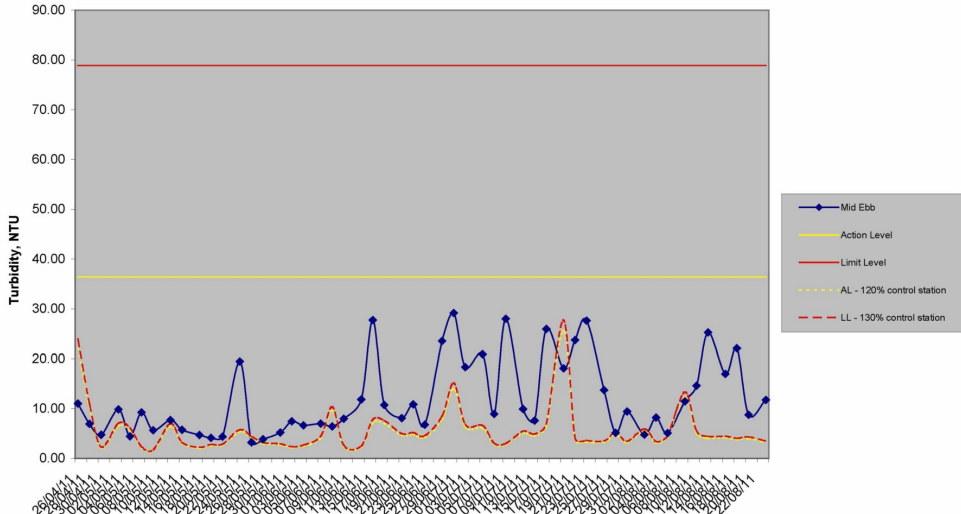


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W1 - Turbidity (Mid-Flood)

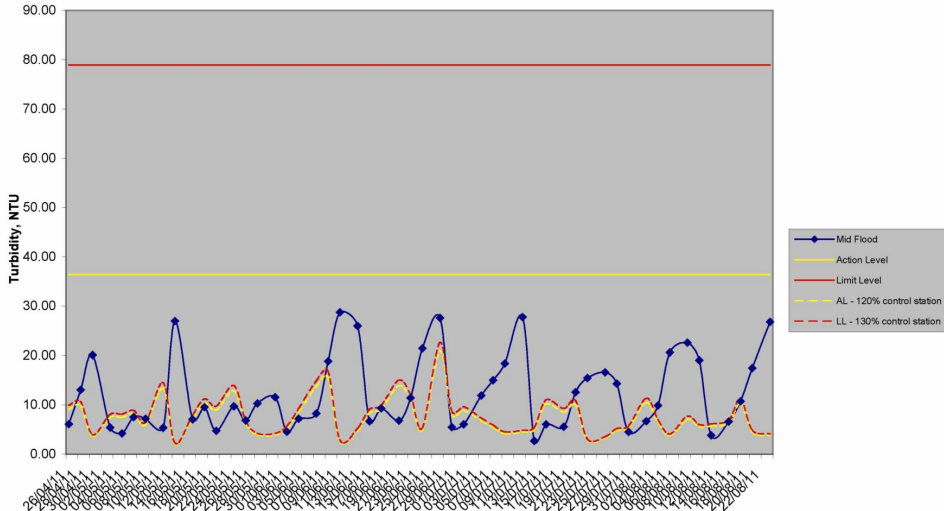


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W1 - pH

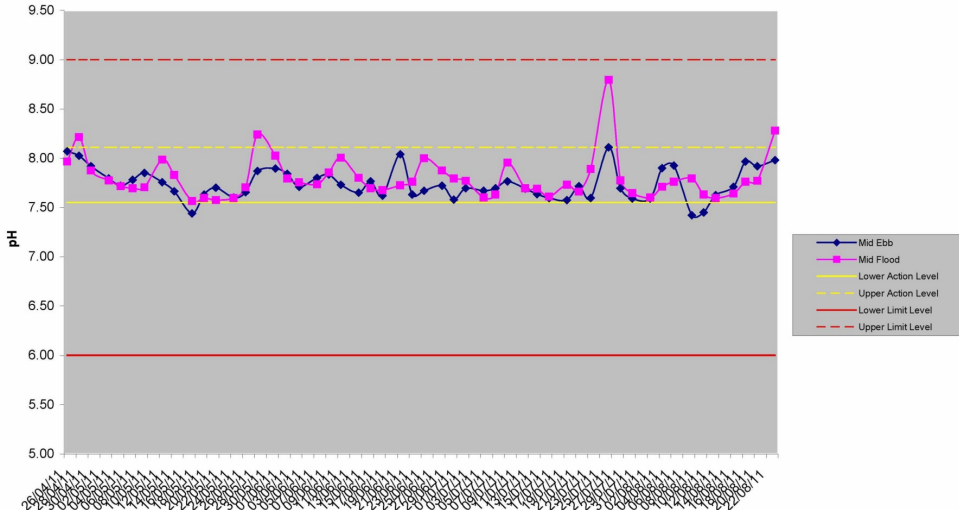


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W1 - Suspended Solid Content (Mid-Ebb)

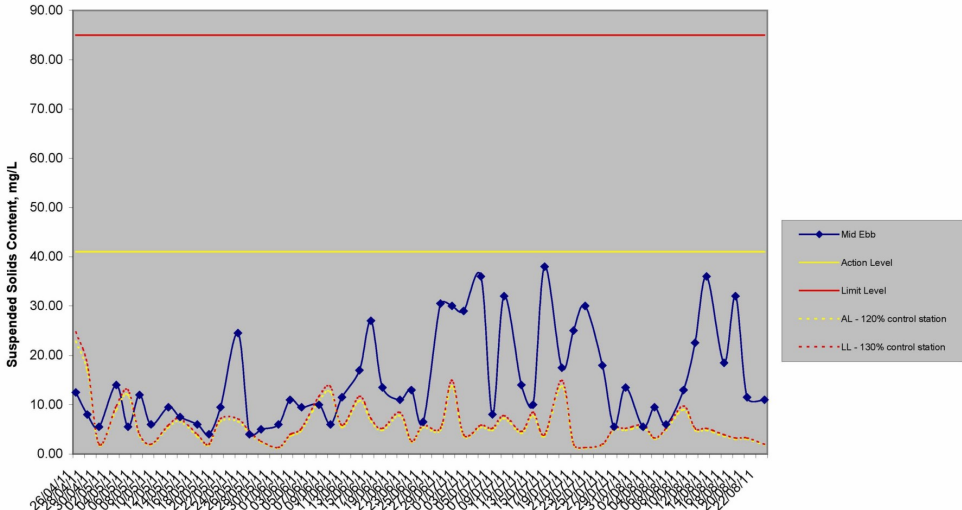

### W1 - Suspended Solids Content (Mid-Flood)

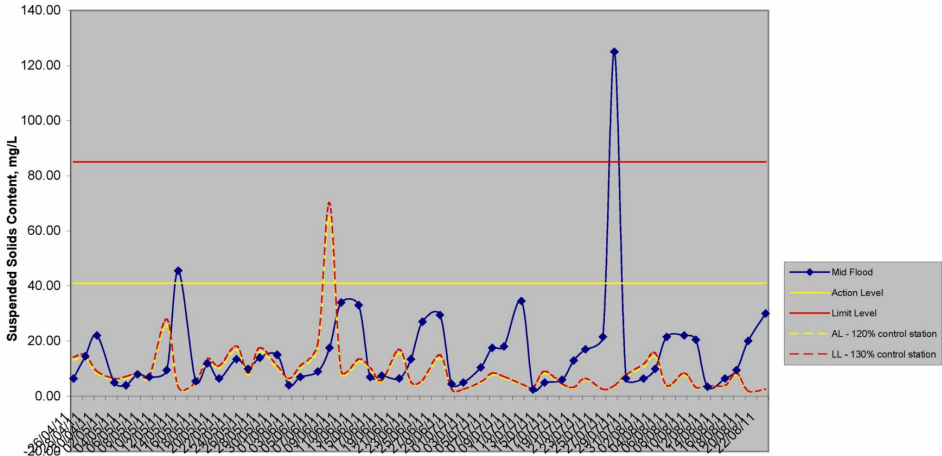


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W2 - Dissolved Oxygen Content

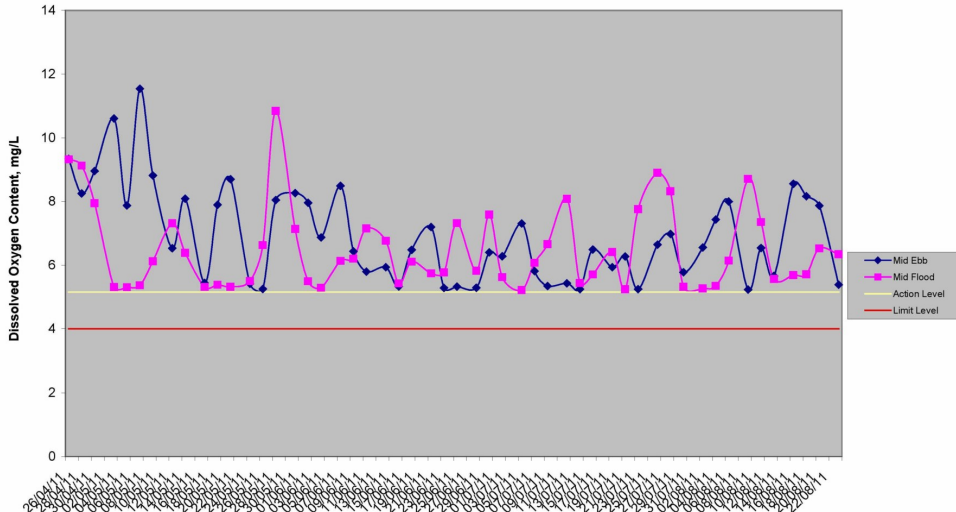


## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



### W2 - Turbidity (Mid-Ebb)

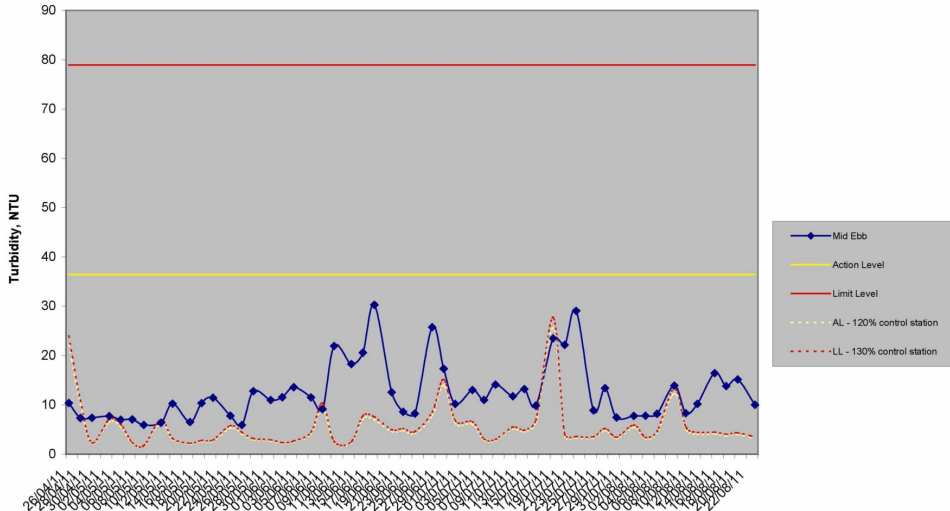




# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W2 - Turbidity (Mid-Flood)

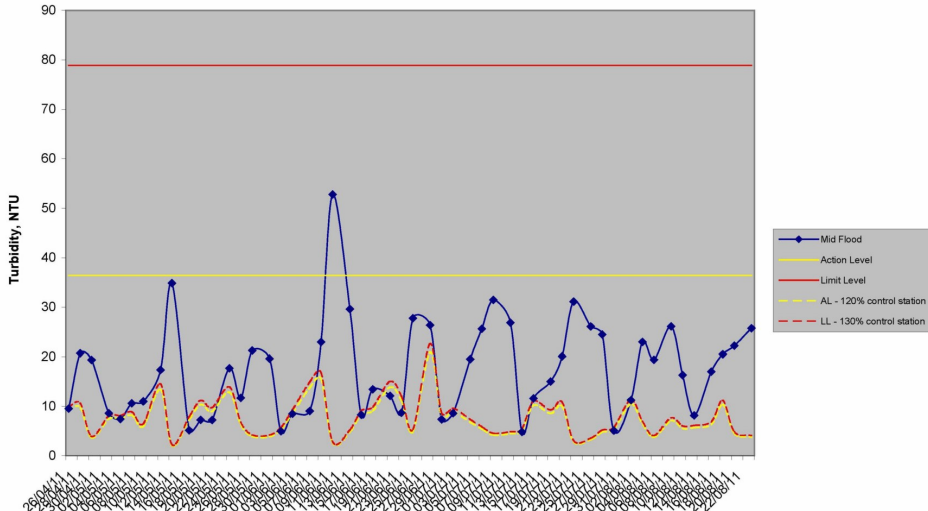


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W2 - pH

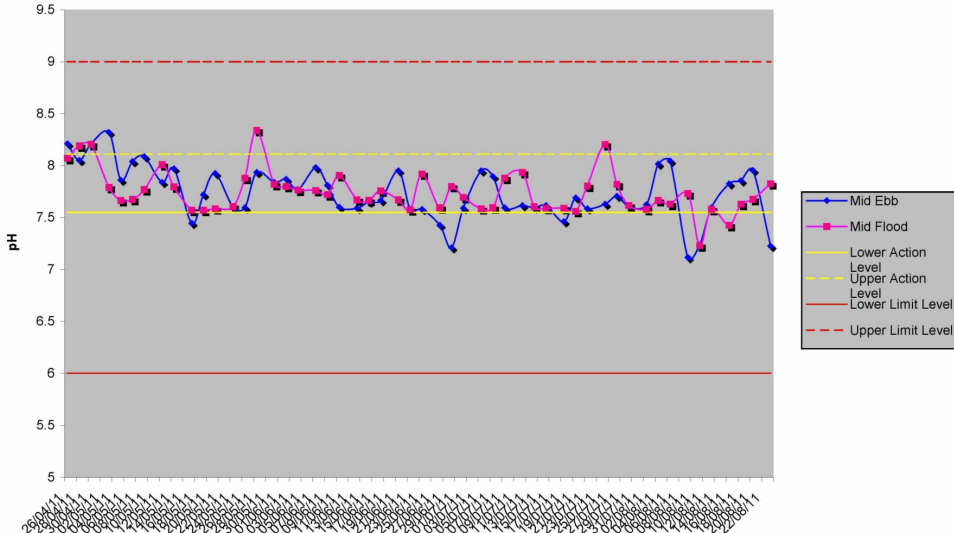


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W2 - Suspended Solids Content (Mid-Ebb)

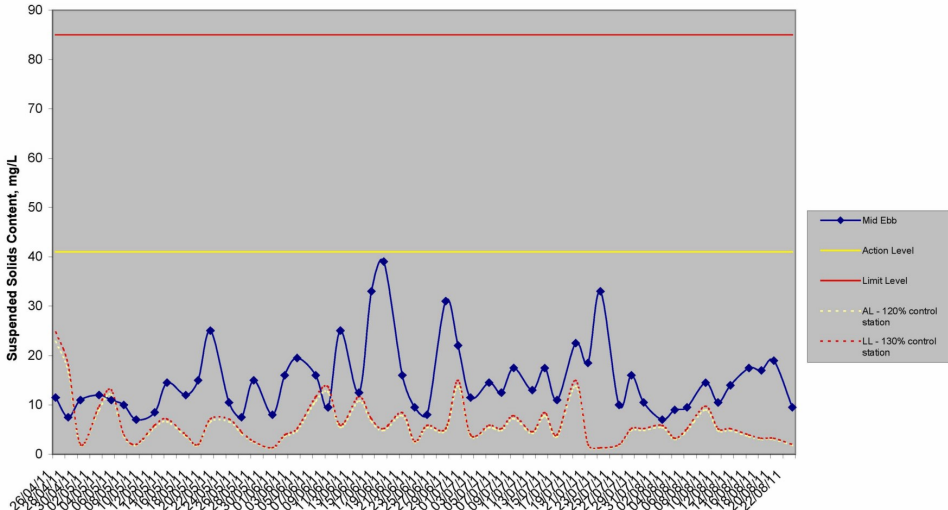

### W2 - Suspended Solids Content (Mid-Flood)

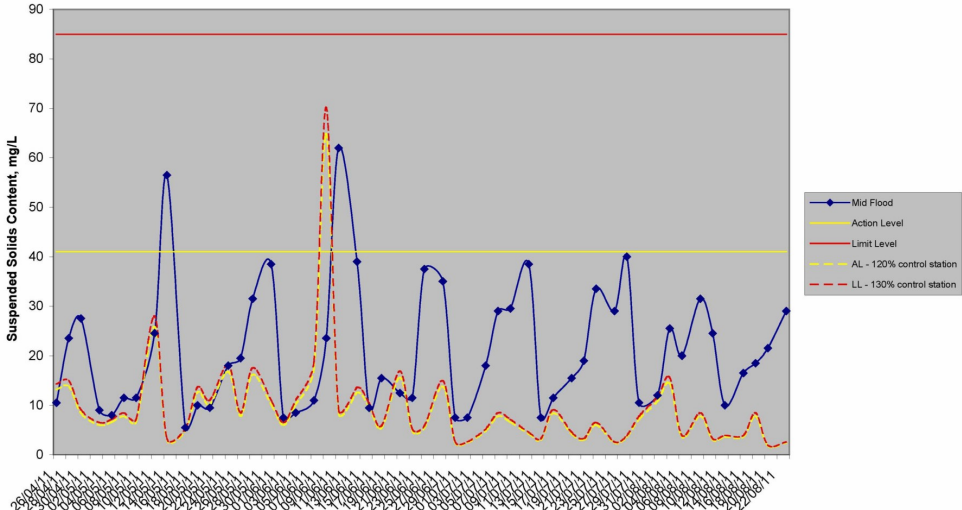


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W3 - Dissolved Oxygen Content

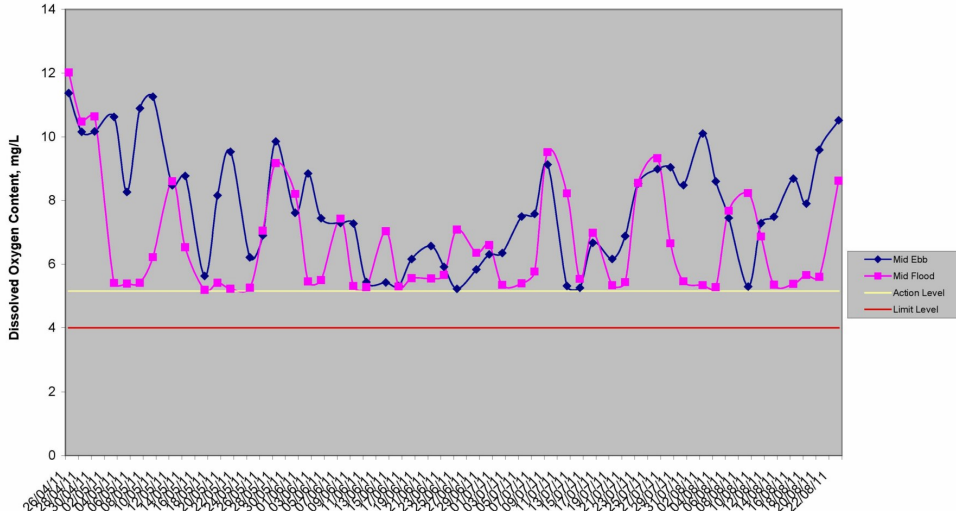

**W3 - Turbidity (Mid-Ebb)**

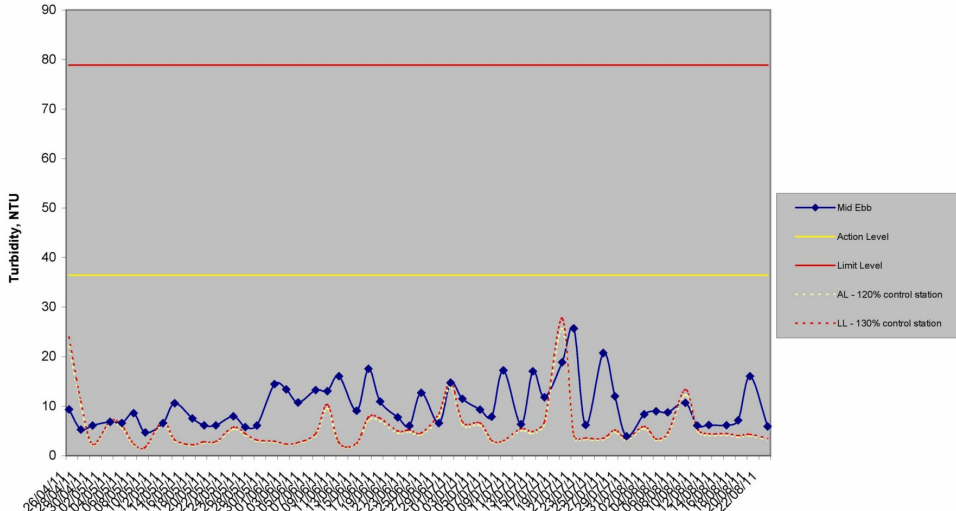


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## W3 - Turbidity (Mid-Flood)

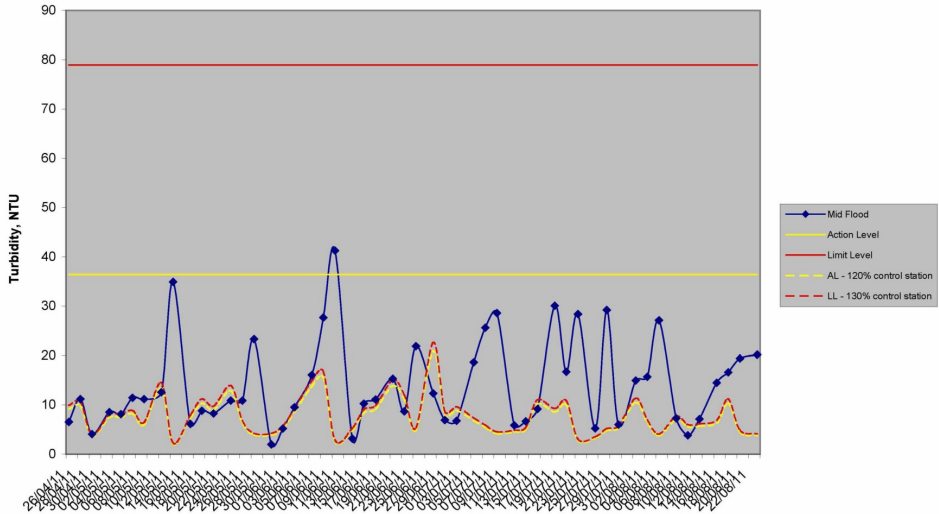


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com




## W3 - pH

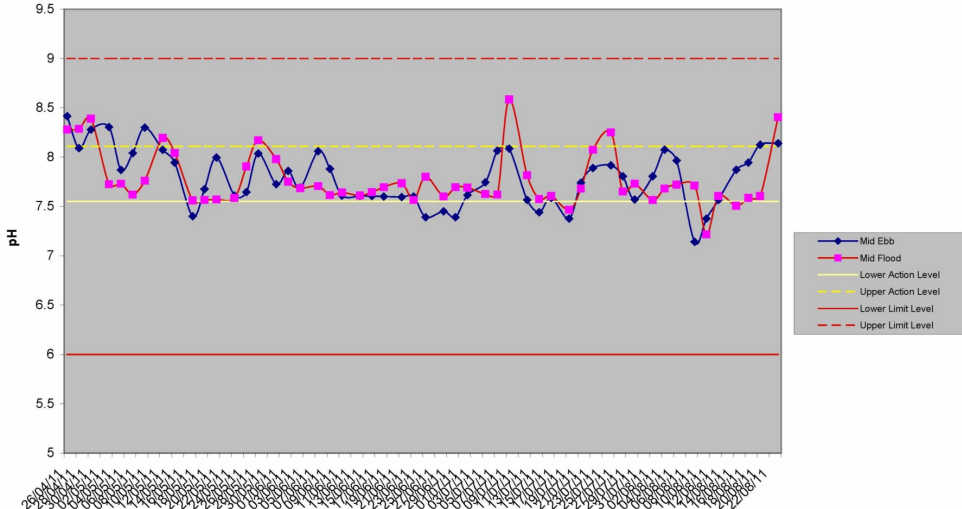





### W3 - Suspended Solids Content (Mid-Ebb)

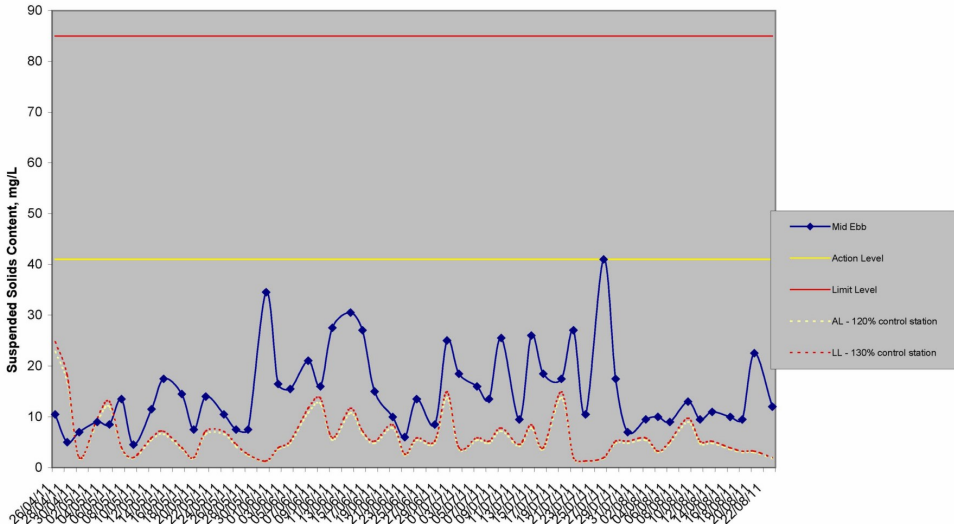

### W3 - Suspended Solids Content (Mid-Flood)

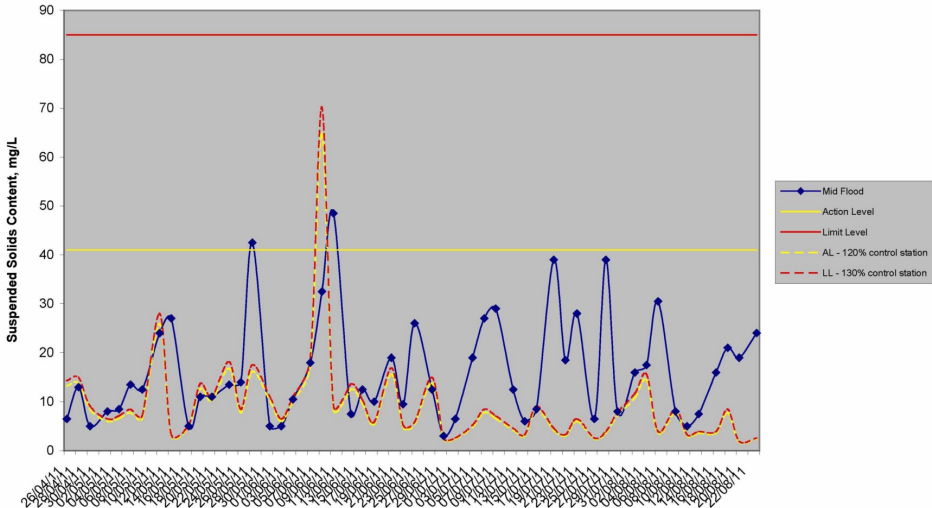

**C1 - Dissolved Oxygen Content**

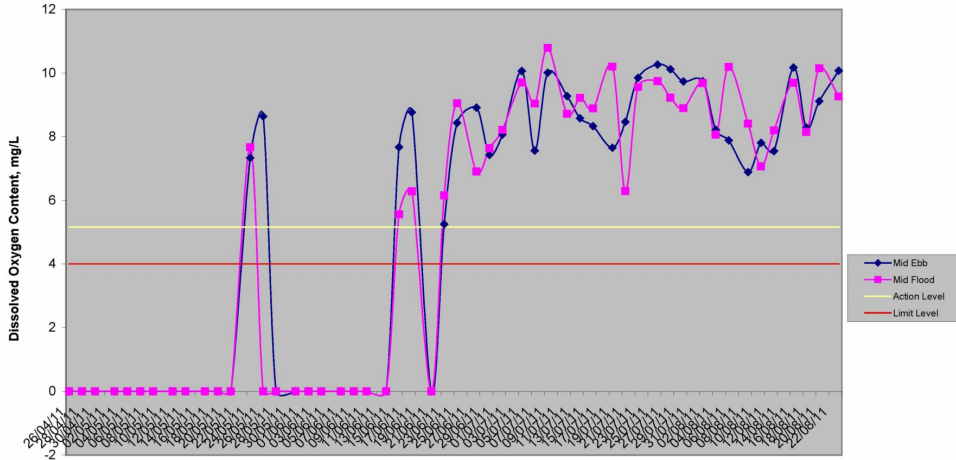

**Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph**


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## C1 - Turbidity

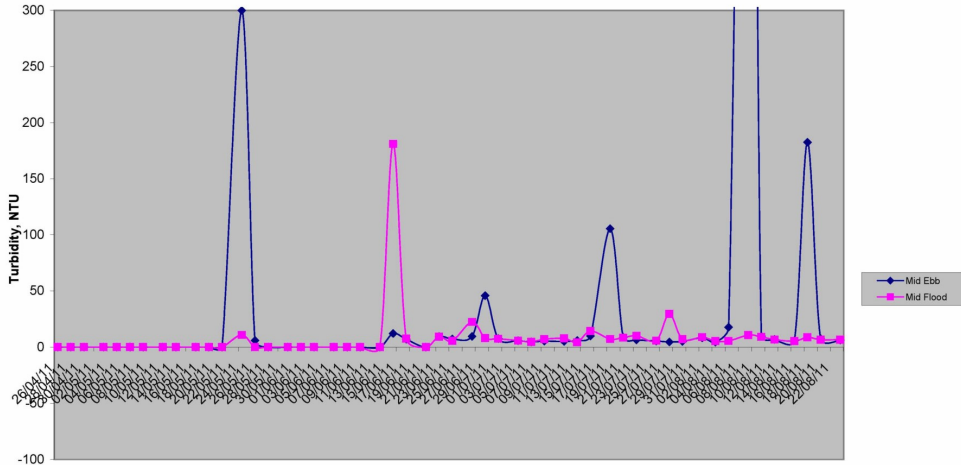

Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## C1 - pH

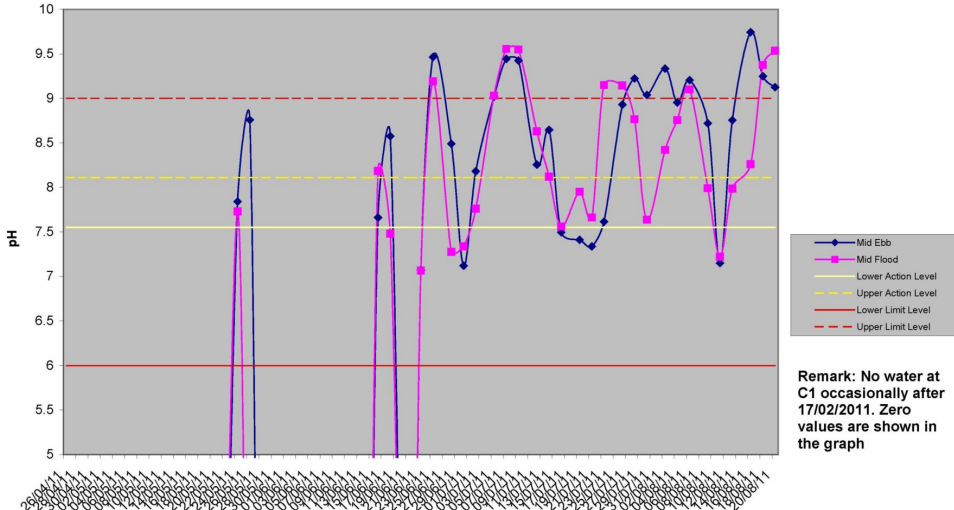

**Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph**


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## C1 - Suspended Solids Content

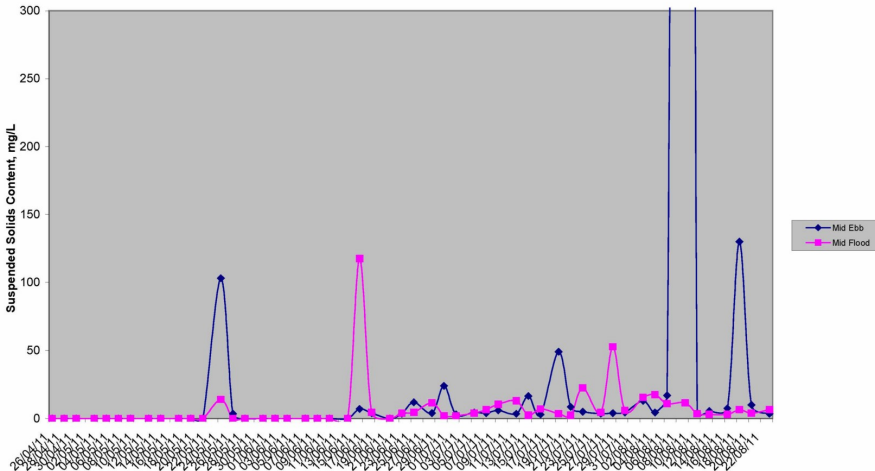

Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## C2 - Dissolved Oxygen Content

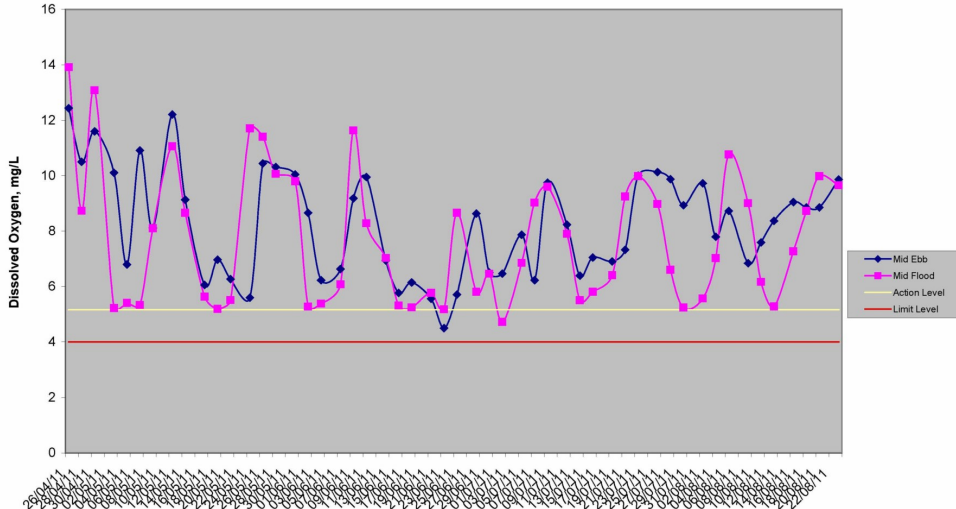


# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## C2 - Turbidity

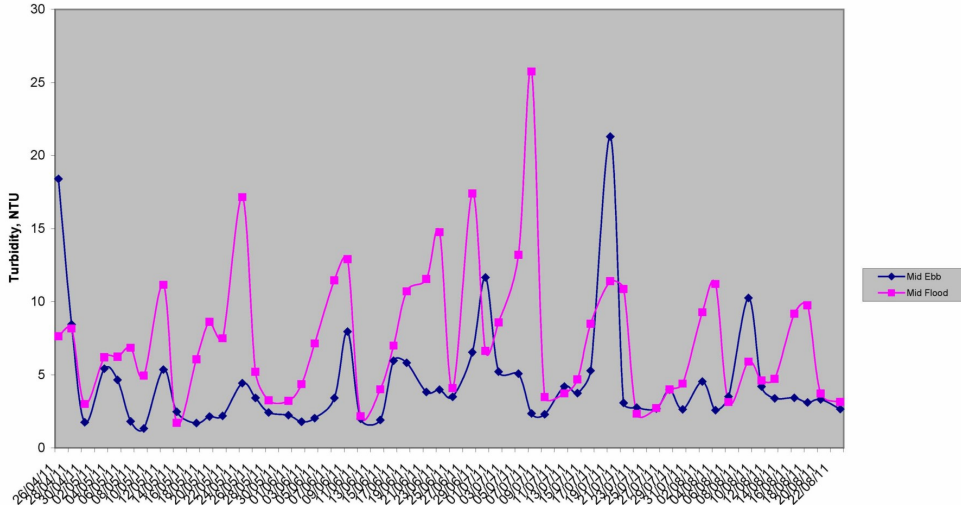




# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
 Fugro Development Centre,  
 5 Lok Yi Street, 17 M.S. Castle Peak Road,  
 Tai Lam, Tuen Mun, N.T., Hong Kong.


Tel : +852-2450 8233  
 Fax : +852-2450 6138  
 E-mail : matlab@fugro.com.hk  
 Website : www.fugro.com



## C2 - pH

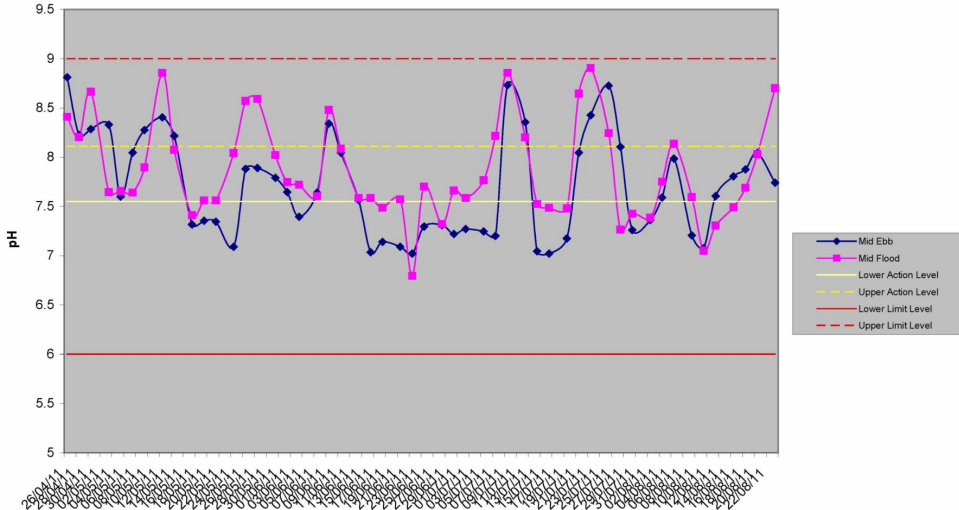

### C2 - Suspended Solids Content

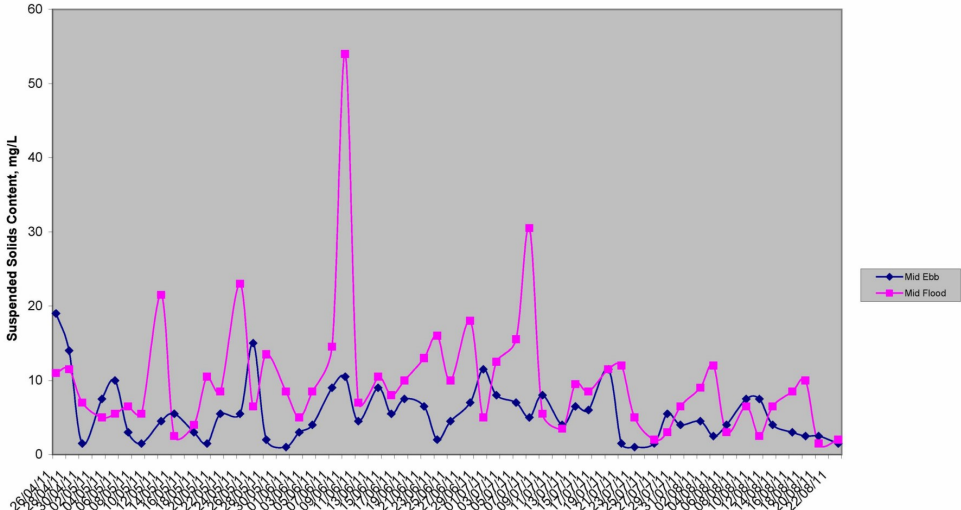

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**


---

### Appendix 5 Construction Program

## HONG KONG SLUDGE TREATMENT FACILITY

### Project Overview

Date	Status	Charted	Approval
02/02/19	SL/AN/PT/22/002/001		

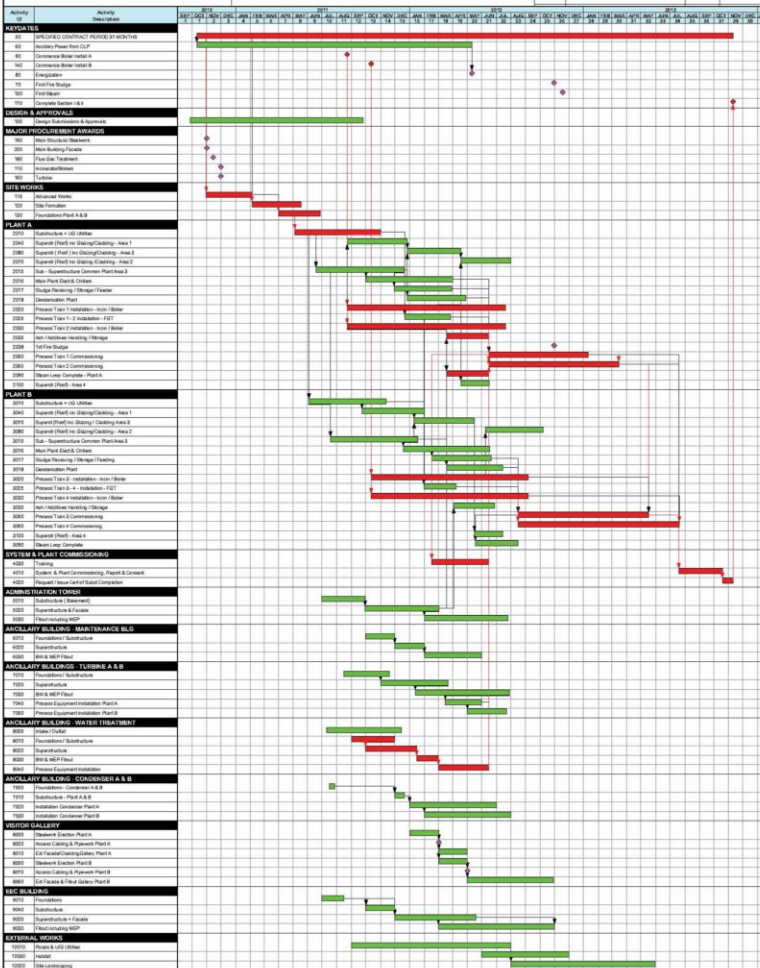

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 6

#### Management Structure and Organization Chart

---

## FUGRO TECHNICAL SERVICES LIMITED


MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

---

### Management Structure and Organization Chart

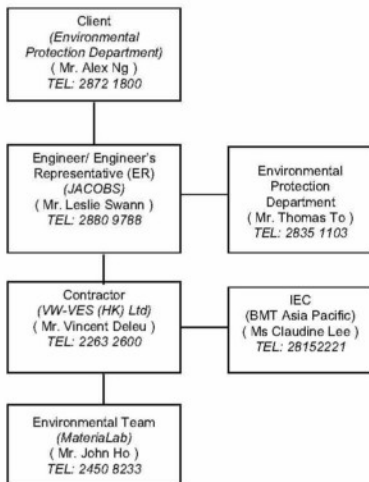

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 7

#### Event / Action Plan for Water Quality

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



## Event/Action Plan for Water Quality

Event	ET Leader	IEC	SOR	Contractor
Action level being exceeded by one sampling day	<ul style="list-style-type: none"> <li>• Repeat <i>in situ</i> measurement to confirm findings;</li> <li>• Identify reasons for non-compliance and source(s) of impact;</li> <li>• Inform IEC and Contractor;</li> <li>• Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>• Discuss mitigation measures with IEC and Contractor;</li> <li>• Repeat measurement on next day of exceedance.</li> </ul>	<ul style="list-style-type: none"> <li>• Discuss with ET and Contractor on the mitigation measures;</li> <li>• Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>• Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>• Discuss with IEC on the proposed mitigation measures;</li> <li>• Make agreement on the mitigation measures to be implemented.</li> <li>• Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>• Inform the SOR and confirm notification of the non-compliance in writing;</li> <li>• Rectify unacceptable practice;</li> <li>• Check all plant and equipment;</li> <li>• Consider changes of working methods;</li> <li>• Discuss with ET and IEC and propose mitigation measures to IEC and SOR;</li> <li>• Implement the agreed mitigation measures.</li> </ul>
Action level being exceeded by more than one consecutive sampling day	<ul style="list-style-type: none"> <li>• Repeat <i>in situ</i> measurement to confirm findings;</li> <li>• Identify reasons for non-compliance and source(s) of impact;</li> <li>• Inform IEC and Contractor;</li> <li>• Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>• Discuss mitigation measures with IEC and Contractor;</li> <li>• Ensure mitigation measures are implemented;</li> <li>• Prepare to</li> </ul>	<ul style="list-style-type: none"> <li>• Discuss with ET and Contractor on the mitigation measures;</li> <li>• Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>• Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>• Discuss with IEC on the Proposed mitigation measures;</li> <li>• Make agreement on the mitigation measures to be implemented;</li> <li>• Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>• Inform the SOR and confirm notification of the non-compliance in writing;</li> <li>• Rectify unacceptable practice;</li> <li>• Check all plant and equipment;</li> <li>• Consider changes of working methods;</li> <li>• Discuss with ET and IEC and propose mitigation measures to IEC and SOR within three working days;</li> <li>• Implement the agreed mitigation measures.</li> </ul>



# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com



	<p>increase the monitoring frequency to daily;</p> <ul style="list-style-type: none"> <li>Repeat measurement on next day of exceedance.</li> </ul>			
Limit level being exceeded by one sampling day	<ul style="list-style-type: none"> <li>Repeat <i>in situ</i> measurement to confirm findings;</li> <li>Identify reasons for non-compliance and source(s) of impact;</li> <li>Inform IEC Contractor and EPD;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>Discuss mitigation measures with IEC, SOR and Contractor;</li> <li>Ensure mitigation measures are implemented;</li> <li>Increase the monitoring frequency to daily until no exceedance of Limit level.</li> </ul>	<ul style="list-style-type: none"> <li>Discuss with ET and Contractor on the mitigation measures;</li> <li>Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>Request Contractor to critically review the working methods;</li> <li>Make agreement on the mitigation measures to be implemented;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>Inform the SOR and confirm notification of the non-compliance in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plant and equipment;</li> <li>Consider changes of working methods;</li> <li>Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days;</li> <li>Implement the agreed mitigation measures.</li> </ul>
Limit level being exceeded by more than one consecutive sampling day	<ul style="list-style-type: none"> <li>Repeat <i>in situ</i> measurement to confirm findings;</li> <li>Identify reasons for non-compliance and source(s) of impact;</li> <li>Inform IEC Contractor and EPD;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> </ul>	<ul style="list-style-type: none"> <li>Discuss with ET and Contractor on the mitigation measures;</li> <li>Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul style="list-style-type: none"> <li>Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>Request Contractor to critically review the working methods;</li> <li>Make agreement on the mitigation measures to be implemented;</li> <li>Assess the effectiveness</li> </ul>	<ul style="list-style-type: none"> <li>Inform the SOR and confirm notification of the non-compliance in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plant and equipment;</li> <li>Consider changes of working methods;</li> <li>Discuss with ET, IEC and SOR and</li> </ul>

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

	<ul style="list-style-type: none"><li>• Discuss mitigation measures with IEC, SOR and Contractor;</li><li>• Ensure mitigation measures are implemented;</li><li>• Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</li></ul>		<p>of the implemented mitigation measures;</p> <ul style="list-style-type: none"><li>• Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.</li></ul>	<p>propose mitigation measures to IEC and SOR within three working days;</p> <ul style="list-style-type: none"><li>• Implement the agreed mitigation measures;</li><li>• As directed by the SOR, to slow down or to stop all or part of the construction activities.</li></ul>
--	---	--	---	--

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 8

#### Implementation Schedule of Mitigation Measures

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 1. Implementation Schedule and Status of Proposed Air Quality Mitigation Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.8.1	<p>Implementation of the Air Pollution Control (Construction Dust) Regulation and good site practices:</p> <ul style="list-style-type: none"> <li>• Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.</li> <li>• Use of frequent watering for particularly dusty construction areas and areas close to ASRs.</li> <li>• Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.</li> <li>• Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.</li> <li>• Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</li> <li>• Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.</li> <li>• Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.</li> </ul>	Work site / During the construction period	Contractor		√			Air Pollution Control (Construction Dust) Regulation

**FUGRO TECHNICAL SERVICES LIMITED**

MaterLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsuen Man, N.T., Hong Kong. Website : www.materlab.com.hk

**MaterLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit.</li> <li>Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.</li> <li>Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>				√			
					√			
					√			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation, and Dec - Decommissioning
- N/A - The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materlab.com.hk


**Table 2. Implementation Schedule of Proposed Human Health Risk Mitigation Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Human Health Risk Associated with Radon</u></p> <p><i>Prevention of radon influx from the PFA to the STF buildings</i></p> <ul style="list-style-type: none"> <li>A soil cover can be provided beneath the buildings on top of ash lagoon prior to construction works because it reduces the level of radon influx significantly</li> <li>Slab-on-grade can be an option on foundation design</li> <li>Soil suction can also prevent radon from entering the building by drawing the radon from below the building and venting it through a pipe, or pipes, to the air above the building.</li> </ul> <p><i>Provision of Sufficient ventilation of the interior of the STF buildings</i></p> <ul style="list-style-type: none"> <li>Forced and natural ventilation should be introduced properly to enhance air exchange rate in the STF buildings.</li> <li>Basement areas should be pressurized by using a fan to blow air into the basement areas from outdoors is suggested. This would create enough pressure at the lowest level indoors to prevent radon from entering into the STF buildings.</li> </ul> <p><i>Regular maintenance for the floor slabs and walls</i></p> <ul style="list-style-type: none"> <li>Cracks and other openings in the foundation should be properly sealed to reduce radon ingress.</li> </ul> <p>Sealing the cracks limits the flow of radon into the building thereby making other radon reduction techniques more effective and cost-efficient. It also reduces the loss of conditioned air.</p>	STF buildings / During the design, construction and operation of the STF.	Contractor / STF Operator		N/A			EPD's ProPECC Note PN 1/99 Control of Radon Concentration in New Buildings Appendix 2
					N/A			
					N/A			
					N/A			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

• N/A - The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 3. Implementation Schedule of Proposed Waste Management Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
SS.5.1	<p><i>Good Site Practices</i></p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> <li>Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>Training of site personnel in proper waste management and chemical handling procedures</li> <li>Provision of sufficient waste disposal points and regular collection of waste</li> <li>Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.</li> </ul>	Work site / During the construction period	Contractor		√			<p>Waste Disposal Ordinance (Cap.354)</p> <p>ETWB TCW No. 19/2005</p>
SS.5.1	<p><i>Waste Reduction Measures</i></p> <ul style="list-style-type: none"> <li>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</li> </ul>	Work site / During planning & design stage, and construction stage	Contractor		√			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,

Fugro Development Centre,

5 Lok Yi Street, 17 M.S. Castle Peak Road,

Tai Lam, Tsun Man, N.T., Hong Kong.

Tel : +852-2450 8233

Fax : +852-2450 6138

E-mail : matlab@fugro.com.hk

Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>The design of the foundation works should minimize the amount of excavated material to be generated.</li> <li>Excavated soil should be reused on site as far as possible, e.g. for landscape works, in order to minimize the amount of public fill to be disposed off-site.</li> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>Encourage collection of aluminium cans by individual collectors by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force</li> <li>Proper storage and site practices to minimize the potential for damage or contamination of construction materials.</li> <li>Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.</li> </ul>				√			
SS.5.1	<p><i>General Refuse</i></p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&amp;D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&amp;D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.</p>	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugo Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
SS.5.1	<p><i>Construction and Demolition Material</i></p> <p>In order to minimize the impact resulting from collection and transportation of C&amp;D material for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below:</p> <ul style="list-style-type: none"> <li>A Waste Management Plan, which becomes part of the Environmental Management Plan, should be prepared in accordance with ETWB TCW No.19/2005.</li> <li>A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed.</li> <li>In order to monitor the disposal of C&amp;D material at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details.</li> </ul>	Work site / During design stage & construction period	Contractor	√	√			ETWB TCW No. 33/2002 ETWB TCW No. 19/2005 ETWB TCW No. 31/2004
SS.5.1	<p><i>Chemical Waste</i></p> <p>If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible</p>	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste)(General) Regulation)

**FUGRO TECHNICAL SERVICES LIMITED**

MaterLab Division, Tel : +852-2450 8233  
 Puro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materlab.com.hk

**MaterLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.							

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des – Design, C – Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk


**Table 4. Implementation Schedule of Proposed Land Contamination Preventive Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
SS.6.3	<b>Fuel Oil Tank Construction and Test</b> <ul style="list-style-type: none"> <li>The fuel tank to be installed should be of specified durability</li> <li>Double skin tanks are preferable</li> <li>Underground fuel storage tank to be installed should be placed within a concrete pit</li> <li>The concrete pit shall be accessible to allow regular tank integrity tests to be carried out at regular intervals</li> <li>The tank integrity tests should be conducted by an independent qualified surveyor or structural engineer</li> <li>Any potential problems identified in the test should be rectified as soon as possible</li> </ul>	Fuel Oil Storage Tank /	Contractor/ STF Operator	√	√ √ N/A √ √ √			
SS.6.3	<b>Fuel Oil Pipeline Construction and Test</b> <ul style="list-style-type: none"> <li>Installation of aboveground fuel oil pipelines is preferable; if underground pipelines are unavoidable, concrete lined trenches should be constructed to contain the pipelines</li> <li>Double skin pipelines are preferable</li> <li>Distance between the fuel oil refuelling points and the fuel oil storage tank shall be minimized</li> <li>The integrity tests for the pipelines should be conducted by an independent qualified surveyor or structural engineer at regular intervals</li> <li>Any potential problems identified in the test should be rectified as soon as possible</li> </ul>	Fuel Oil Pipelines/ Design, Construction and Operation Phase	Contractor/ STF Operator	√	√ √ √ √ √			
SS.6.3	<b>Fuel Oil Leakage Detection</b> <ul style="list-style-type: none"> <li>Installation of leak detection device at storage tank and pipelines</li> </ul>	Fuel Oil Storage Tank	Contractor/ STF Operator	N/A	N/A			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation, and Dec - Decommissioning
- N/A - The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 5. Implementation Schedule of Proposed Water Pollution Control Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.2	<b>Construction Runoff and Drainage</b> <ul style="list-style-type: none"> <li>Site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" shall be followed as far as practicable in order to minimize surface runoff and the chance of erosion:</li> <li>At the start of site establishment, internal drainage works and erosion and sedimentation control facilities shall be implemented. Channels, earth bunds or sand bag barriers shall be provided on site to direct stormwater to silt removal facilities. The detailed design and installation of the temporary on-site drainage system shall be undertaken by the contractor prior to the commencement of construction.</li> <li>Before commencing any site formation work, all sewer and drainage connections shall be sealed to prevent debris, soil, sand etc. from entering public sewers/drains.</li> <li>Boundaries of earthworks shall be surrounded by dykes or embankments for flood protection, as necessary.</li> <li>Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove sand/silt particles from runoff to meet the standards of the Technical</li> </ul>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO
					N/A			
					√			
					√			
					√			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>Memorandum under the Water Pollution Control Ordinance. The design of silt removal facilities shall be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures shall be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</p> <ul style="list-style-type: none"> <li>Water pumped out from foundation piles shall be discharged into silt removal facilities.</li> <li>During rainstorms, exposed slope/soil surfaces shall be covered by a tarpaulin or other means, as far as practicable. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94.</li> <li>Exposed soil areas shall be minimized to reduce potential for increased siltation and contamination of runoff.</li> <li>Earthwork final surfaces shall be well compacted and subsequent permanent work or surface protection shall be immediately performed. Open stockpiles of construction materials or construction wastes on-site of more than 50m<sup>3</sup> shall be covered with tarpaulin or similar fabric during rainstorms.</li> <li>All vehicles shall be cleaned before leaving the works area to ensure no earth, mud and debris is deposited on roads. An adequately designed and</li> </ul>				N/A			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	sited wheel washing bay shall be provided at every site exit. The wheel washing facility shall be designed to minimize the intake of surface water (rainwater). Wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process.							
S6.7.2	<p><i>General Construction Activities</i></p> <ul style="list-style-type: none"> <li>Debris and refuse generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby water bodies and public drainage system. Stockpiles of cement and other construction materials shall be kept covered when not being used.</li> <li>Oils and fuels shall only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to nearby water bodies and public drains, all fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund shall be drained of rainwater after a rain event.</li> </ul>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94;
S6.7.2	<p><i>Sewage Effluents</i></p> <ul style="list-style-type: none"> <li>Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.</li> </ul>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugo Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.2	<p><i>Release of PFA Leachate from Ash Lagoon into the Aquatic Environment</i></p> <ul style="list-style-type: none"> <li>Environmental monitoring and audit (EM&amp;A) should be included to ensure that the foundation construction would not cause an unacceptable release of PFA leachate into the Deep Bay waters. The parameters to be measured should include the heavy metals such as cadmium, chromium and aluminium, which have the greatest tendency to leach from the lagooned PFA into the seawater. Details of the measurement requirements are presented in the EM&amp;A manual</li> </ul>	<p>Deep Bay</p> <p>Water outside the Ash Lagoon / During the construction period</p>	Contractor		√			WPCO

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and/or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation, and Dec - Decommissioning
- N/A - The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 6. Implementation Schedule of Proposed Ecological Mitigation Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S7.8.2	Measures to Minimize Disturbance Impact to Wildlife <ul style="list-style-type: none"> <li>Hoarding of 3m high shall be set up along the boundary of the works areas and associated site access to shield the fauna and breeding population of Little Grebe in the Middle Lagoon from the disturbance impact of machinery.</li> <li>The works boundaries shall not go beyond the proposed Project Area. All work crews, equipment and human activities shall be confined within the designated works area only. No personnel should encroach or wilfully disturb any wild animals and their habitats. Traffic and human access from the western side of the Project Area should be avoided.</li> <li>Fencing with climbers or plantation shall be provided, where appropriate, along the STF site boundary and the two sides of access road to screen the surrounding habitats from the STF works areas.</li> </ul>	Boundary of works areas/ Construction Phase	Contractor		√			
		Boundary of works areas/ Construction Phase	Contractor		√			
		Boundary of works areas/ Operation Phase	Contractor		√			



**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	
				Des	C	O	Dec		
S7.8.2	Measures to Minimize Impact to natural habitats <ul style="list-style-type: none"> <li>Where practicable, all proposed works shall be conducted in existing built up area to minimize impact to natural habitats.</li> <li>The abutment (permanent structure) for the vehicular bridge shall avoid streambed. The number and size of the temporary supporting structures to be installed over the streambed during construction shall be minimized as far as practicable.</li> <li>The temporarily affected natural habitats, including streambed, shall be reinstated after the completion of works.</li> <li>For affected natural stream section, placement of substrates of similar size and composition to those of original streambed shall be considered to encourage colonization.</li> </ul>	Works areas/ Design and Construction Phase  Vehicular bridge/ Design and Construction Phase  Works Area/ Operation Phase  Works Area/ Operation Phase	STF Designer/ Contractor  STF Designer/ Contractor  Contractor  Contractor	√  √  N/A  N/A	√  N/A  N/A				ETWB TC (Works)  No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works
S7.8.2	<i>Minimise sedimentation/water quality impacts to waterbodies</i> <ul style="list-style-type: none"> <li>Measures to control potential sedimentation/ water quality impacts during the construction phase shall be implemented.</li> <li>To minimize the potential water quality impacts from the construction works located at any river channels, natural streams or seafront, the practices outlined in</li> </ul>	Whole Site/ Construction Phase	Contractor		√  √			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works	

**FUGRO TECHNICAL SERVICES LIMITED**

MaterLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materlab.com.hk

**MaterLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	ETWB TC (Works) No. 5/2005 "Protection of natural streams/ rivers from adverse impacts arising from construction works" shall be adopted where applicable.							
S7.8.2	<p><i>Minimize noise disturbance</i></p> <ul style="list-style-type: none"> <li>Noise mitigation measures including the use of quieter piling machinery and construction plants shall be implemented to lower the noise level due to construction works.</li> <li>Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction programme.</li> <li>Machines and plant which may be in intermittent use shall be shut down to a minimum.</li> <li>Plant known to emit noise strongly in one direction, shall be oriented so that the noise is directed away from the Middle Lagoon, where possible.</li> <li>Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction period.</li> <li>Mobile plant (such as generator) shall be sited as far away from the Middle Lagoon as possible.</li> <li>Material stockpiles and other structures shall be effectively utilized, where practicable, to screen noise from on-site construction activities.</li> </ul>	Whole Site/ Construction Phase	Contractor		√			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works
					√			
					√			
					√			
					N/A			
					√			
					√			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S7.8.3	<p><i>Measures to Mitigate the Loss of Vegetation</i></p> <ul style="list-style-type: none"> <li>All vegetation located within the work areas shall be preserved as far as practicable.</li> <li>To compensate for the loss of the vegetation and habitats, tree planting shall be provided in the site area where possible. Species chosen for planting shall be similar to the species identified in the survey and be native to Hong Kong or the Southern China.</li> </ul>	Whole Site / Design, Construction and Operation Phase	Contractor / STF Operator	√	√			
S7.8.4	<p>Enhancement Measures to Create Additional Habitat for Little Grebe</p> <ul style="list-style-type: none"> <li>An additional habitat for Little Grebe shall be created in a less disturbed area located at the northeastern part of the proposed STF.</li> <li>The created habitat shall be provided in form of shallow pond(s) incorporating suitable habitat characteristics for Little Grebe. The water level of the created pond shall be kept between 1.5 m to 2 m.</li> <li>Emergent vegetation shall be planted and fish population shall be controlled to allow development of aquatic invertebrate populations as prey of Little Grebe.</li> <li>To screen the created habitat from disturbance due to nearby landfill traffic, planting of native plants shall be provided on the boundary of the pond(s) as appropriate.</li> <li>Prior to construction of the pond(s), detailed Habitat Creation and Management Plan (HCMP) of the created habitat prepared by experienced ecologist(s) with over seven year experience in relevant field shall be circulated to relevant departments including AFCDD for comment.</li> </ul>	Within Project Area/ Design Phase, Construction and Operation Phase	Contractor / STF Operator	√	N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec - Decommissioning
- N/A - The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 7. Implementation Schedule for Landscape and Visual Impact**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
T able 9.4 CM-01	<u>Contaminant/ Sediment Control</u> – Suitable temporary barriers, covers and drainage provisions shall be provided around construction works to avoid discharge of contaminants (such as bleeding from in-situ concrete works) and sediments into sensitive water-based habitats, especially the tidal streams and the mangrove.	Work site / During the construction period	Contractor		√			
T able 9.4 CM-02	<u>Early Planting of Tall Trees</u> – Tall trees proposed under mitigation measure OM-02 shall be planted early, providing visual effect also during construction.	Work site / During the construction period	Contractor		N/A			
T able 9.4 CM-03	<u>Good Site Practice</u> – Construction activities should be restricted to works areas and should be clearly demarcated onsite. Piling of construction materials onsite shall be carefully considered for possible impacts before carrying out.	Work site / During the construction period	Contractor		√			
T able 9.4 CM-04	<u>Existing Trees within Works Areas</u> – All existing trees within work sites shall be properly maintained and protected for their crowns, trunks and roots.	Work site / During the construction period	Contractor	√	√			
T able 9.4 OM-01	<u>Sensitive Bridge Design</u> – The bridge of the proposed access road shall be sensitively designed to minimize impact to the tidal stream and mangrove. It shall be constructed with minimal use of in-situ concreting and with maximum use of precast or prefabricated elements. No pile or support shall be erected within the stream channel.	Bridge of access road / During the design & construction phases	Contractor	√	N/A			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Fugro Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 9.4 OM-02	<u>Tall trees for Chimney</u> – Fast-growing tall trees shall be planted along the east side of the ash-lagoon to counterbalance possible exotic silhouettes, such as from the chimney, of the proposed sludge treatment facilities for sensitive viewers in Pak Nai. The trees shall be planted during the early stage of the construction to ensure effectiveness during operation. They will also help to lessen the visual impact during construction, as already suggested in mitigation measure CM-02.	East side of ash lagoon / During the design & construction phases	Contractor	√	N/A			
Table 9.4 OM-03	<u>Suitable Reinstatement at Ash-lagoon</u> – Affected perimeter of the proposed works area within the ash-lagoon shall be reinstated with suitable planting materials. Traditional reinstatement planting approach for construction projects may not work well for this project. Certain existing grasses and small shrubs have self-seeded the ash-lagoon, demonstrating their tolerance to salts, alkalinity and possible trace metals in the ash. Therefore the same or similar species of vegetation shall be used.	Perimeter of works area / During the design & construction phases	Contractor	√	N/A			
Table 9.4 OM-04	<u>Existing Tree Transplanting</u> – The proposed access roadworks may affect few existing trees, which shall be transplanted as far as practical. A comprehensive tree survey is recommended to locate these trees.	Access road / During the design & operation phases	Contractor	√	N/A			
Table 9.4 OM-05	<u>Planting at Road Intersection</u> – Suitable planting of woodland trees and shrubs shall be provided for the proposed access roadworks at the junction with Nim Wan Road.	Junction of access road with Nim Wan Road / During the design & operation phases	Contractor	√	N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec - Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugo Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab****Table 8. Implementation Schedule of Proposed Landfill Gas Hazard Protection Measures**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S10.7.2	<b>Appointment of Safety Officer</b> Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard.	Work Site / During the construction phase	Contractor		√			
S10.7.2	<b>Safety Measures - Excavation</b> Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.	Work Site / During the construction phase	Contractor		√			
S10.7.2	<b>Safety Measures – Welding, Flame-Cutting and Hot works</b> Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, “permit to work” procedures should be followed.	Work Site / During the construction phase	Contractor		√			
S10.7.2	<b>Safety Measures – Enclosed Spaces</b> Site offices or buildings located within WENT Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Enclosed Spaces within WENT Consultation Zone / During the construction phase	Contractor		N/A			
S10.7.2	<b>Safety Measures – Electrical Equipment</b> Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Work Site / During the construction phase	Contractor		N/A			

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division, Tel : +852-2450 8233  
 Pugno Development Centre, Fax : +852-2450 6138  
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk  
 Tai Lam, Tsun Man, N.T., Hong Kong. Website : www.materiallab.com.hk

**MaterialLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S10.7.2	<b>Safety Measures – Piping</b> During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Work Site / During the construction phase	Contractor		N/A			
S10.7.2	<b>Safety Measures – Fire Safety</b> Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be posted around the site warning the anger and potential hazards.	Work Site / During the construction phase	Contractor		√			
S10.7.2	<b>Safety Measures – Confined Spaces</b> Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined Spaces at Work Site / During the construction phase	Contractor		N/A			
S10.7.2	<b>Monitoring</b> Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored shall be set down prior to commencement of ground-works. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 10.6 of the EIA Report.	Work Site / During the construction phase	Contractor		N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec - Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

### Appendix 9

#### Incident Report on Action Level or Limit Level Non-compliance



**FUGRO TECHNICAL SERVICES LIMITED**

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233  
Fax : +852-2450 6138  
E-mail : mallab@fugro.com.hk  
Website : www.materiabl.com.hk

**MateriaLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

**Incident Report on Action Level or Limit Level Non-compliance**

Project	Sludge Treatment Facilities
Date	26 July 2011
Time	09:30 to 10:30 (Mid-Ebb)
Monitoring Location	W3
Parameter	Suspended solids content
Action & Limit Levels	Action Level : $\geq 41$ mg/L and 120% of control station (i.e. C1: 5 mg/L; C2: 18 mg/L) Limit Level : $\geq 85$ mg/L and 130% of control station (i.e. C1: 5 mg/L; C2: 20 mg/L)
Measured Level	W3 : 41 mg/L (exceed Action Level) C1 : 3.5 mg/L C2 : 1.5 mg/L
Possible reason for Action or Limit Level Non-compliance	Piling at North part of the Lagoon and far away from the stream.  Exceedance is not related to construction activity but was due to occasional collection of dense solid particles at W3 as the low turbidity was taken at W3 during the same sampling period.
Actions taken / to be taken	The exceedance was not related to the site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 29 July 2011

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	26 July 2011
Time	10:34 to 11:28 (Mid-ebb)
Monitoring Location	W1
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W1 : 8.11 (exceed Action Level) C1 : 8.93 C2 : 8.73
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance was subject to the influent of the high pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 4 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	26 July 2011
Time	<sup>16:29</sup> 10:34 to <sup>17:54</sup> 11:28 (Mid-ebb) <sup>Flood</sup> ✓
Monitoring Location	W1, W2, W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W1 : 8.8 (exceed Action Level) W2 : 8.2 (exceed Action Level) W3 : 8.3 (exceed Action Level) C1 : 9.2 C2 : 8.3
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance was subject to the influent of the high pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ETI Leader)

Signature : 

Date : 4 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

**FUGRO TECHNICAL SERVICES LIMITED**

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

**Incident Report on Action Level or Limit Level Non-compliance**

Project	Sludge Treatment Facilities
Date	28 July 2011
Time	17:40 to 18:02 (Mid-flood)
Monitoring Location	W1
Parameter	Suspended solids content
Action & Limit Levels	Action Level : $\geq 41$ mg/L and 120% of control station (i.e. C1: 64 mg/L ; C2: 4 mg/L) Limit Level : $\geq 85$ mg/L and 130% of control station (i.e. C1: 69 mg/L ; C2: 4 mg/L)
Measured Level	W1 : 125 mg/L (exceed Limit Level) C1 : 53 mg/L C2 : 3 mg/L
Possible reason for Action or Limit Level Non-compliance	Piling at North part of the Lagoon and far away from the stream.  Exceedance is not related to construction activity, it was due to stirring up of seabed materials near W1 when the Deep Bay water surface became rough after Typhoon Signal No.1 was hoisted.
Actions taken / to be taken	The exceedance was not related to the site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 01 August 2011

**CONFIDENTIALITY NOTICE**

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	09 August 2011
Time	9:41 to 11:05 (Mid-ebb)
Monitoring Location	W1, W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W1 : 7.42 (exceed Action Level) W2 : 7.12 (exceed Action Level) W3 : 7.14 (exceed Action Level) C1 : 8.72 C2 : 7.21
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W1, W2 and W3 were subject to the influent of the low pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 11 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	11 August 2011
Time	11:32 to 12:47 (Mid-ebb)
Monitoring Location	W1, W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W1 : 7.45 (exceed Action Level) W2 : 7.24 (exceed Action Level) W3 : 7.38 (exceed Action Level) C1 : 7.15 C2 : 7.08
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W1, W1 and W3 were subject to the influent of the low pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 15 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	11 August 2011
Time	16:55 to 17:57 (Mid-flood)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W2 : 7.23 (exceed Action Level) W3 : 7.22 (exceed Action Level) C1 : 7.22 C2 : 7.05
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W2 and W3 were subject to the influent of the low pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 15 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	16 August 2011
Time	8:48 to 10:48 (Mid-flood)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W2 : 7.43 (exceed Action Level) W3 : 7.51 (exceed Action Level) C1 : 8.26 C2 : 7.49
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W2 and W3 were subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)  
Signature :   
Date : 17 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)



# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	23 August 2011
Time	8:40 to 10:23 (Mid-Ebb)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W2 : 7.23 (exceed Action Level) W3 : 8.14 (exceed Action Level) C1 : 8.93 C2 : 7.74
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W2 was subject to local influent of surface runoff due to raining. The lowered pH level at C2 would be the same reason as those at W2 on the same day of water monitoring.  The pH level at W3 remained high in comparison with morning and afternoon monitoring sessions on the same day.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)  
Signature :   
Date : 30 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

# FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

**MaterialLab**

Our Ref. No. : 100440  
Client : VW-VES (HK) Ltd.  
Project : Contract No. EP/SP/58/08

## Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	23 August 2011
Time	15:15 to 16:31 (Mid-Flood)
Monitoring Location	W1 and W3
Parameter	pH
Action & Limit Levels	Action Level : $\leq 7.55$ or $\geq 8.11$ Limit Level : $\leq 6$ or $\geq 9$
Measured Level	W1 : 8.28 (exceed Action Level) W3 : 8.41 (exceed Action Level) C1 : 9.65 C2 : 8.70
Possible reason for Action or Limit Level Non-compliance	Piling in progress but far away from the stream.  The exceedance of W1 and W3 were subject to the influent of the high pH from C1 and C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 30 August 2011

### CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

**Figure 1.1**

**Construction Works Area**

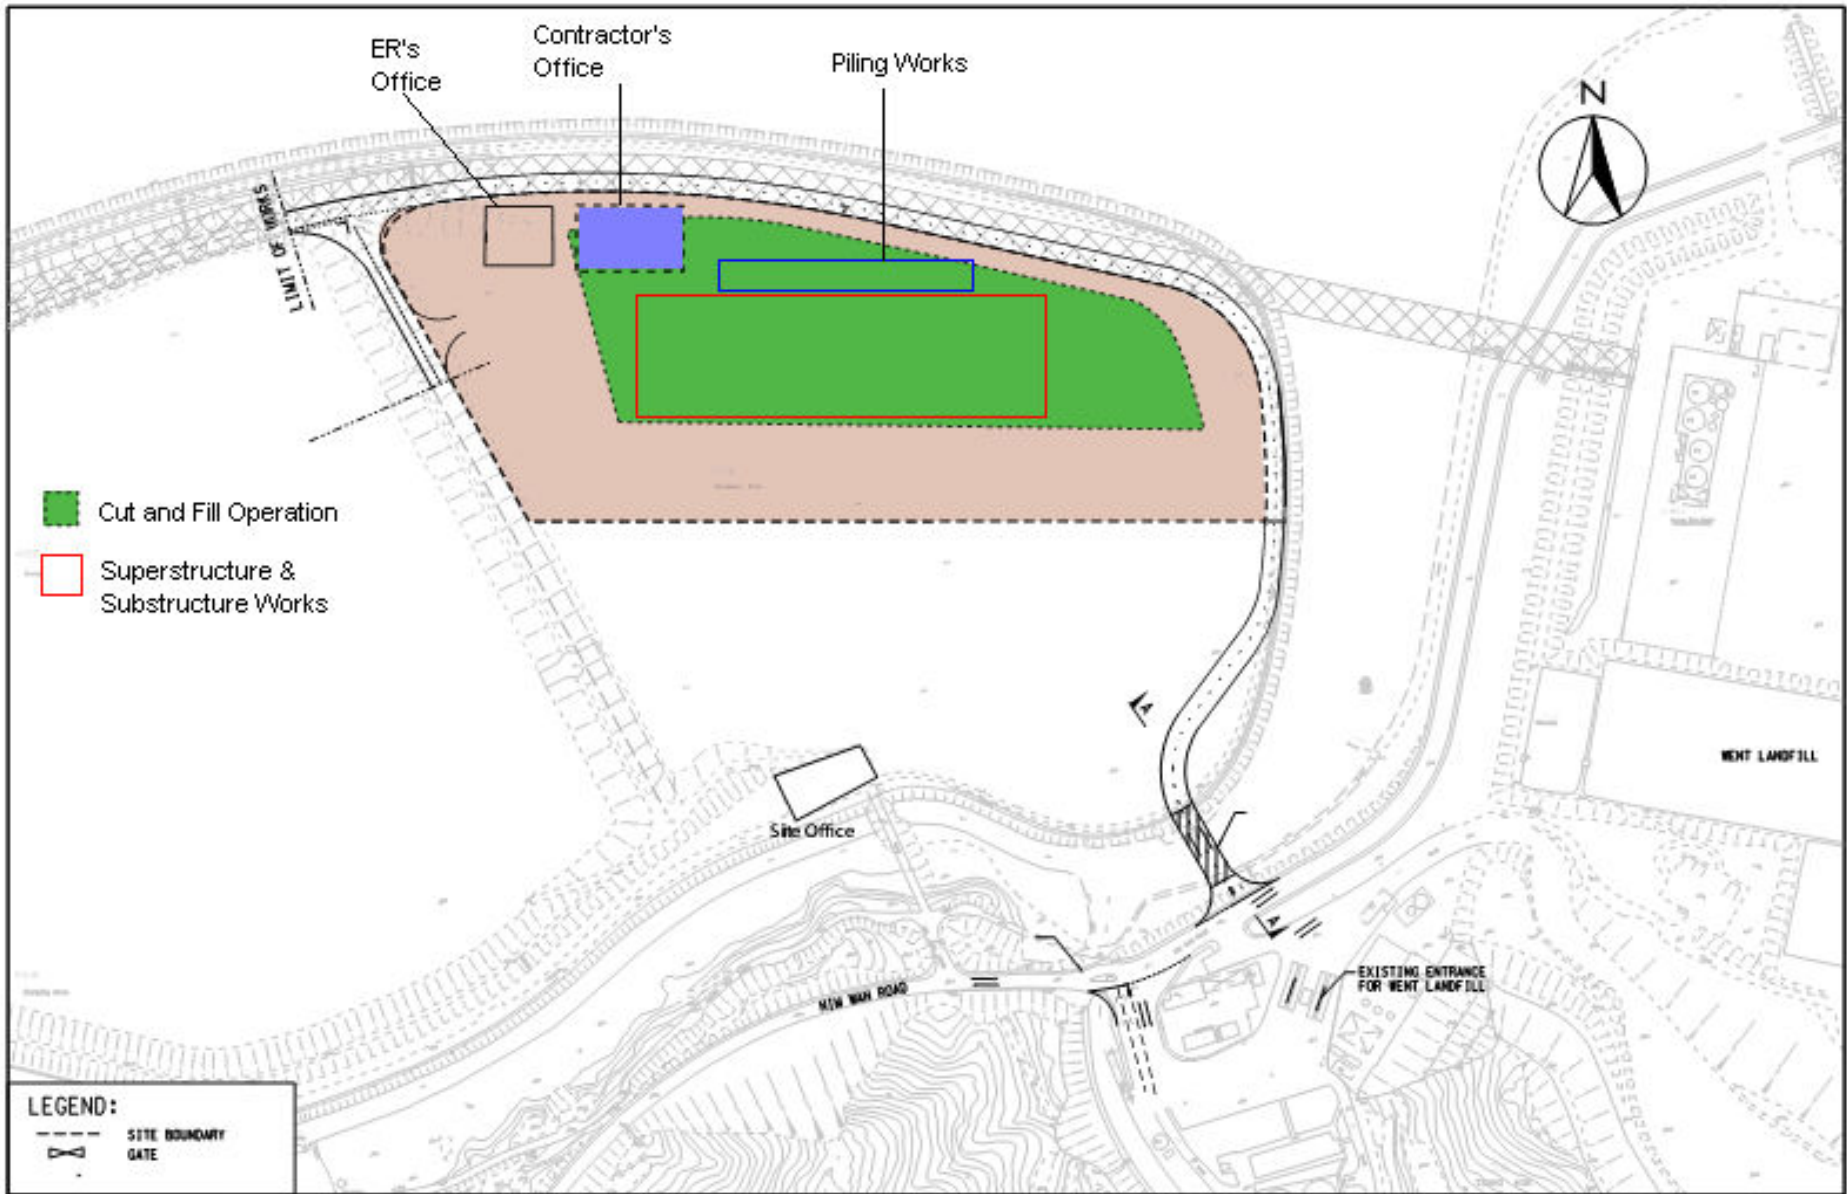

**LEGEND:**

--- SITE BOUNDARY  
 X GATE

MAUNSELL | AECOM  
 Munsell & Day, Inc.

AGREEMENT NO. CE 28/2003 (EP)  
 SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY  
 GENERAL LAYOUT OF PROPOSED SLUDGE TREATMENT FACILITIES (STF)

SCALE	A3 1:2500	DATE	JAN. 2008
CHECK	-	DRAWN	MJM
JOB NO.	60015756	DRAWING NO.	FIGURE 1.1
		REV	-

---

## FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : matlab@fugro.com.hk  
Website : www.fugro.com

---

**MateriaLab**

---

**Figure 3.1**  
**Site Layout Plan**

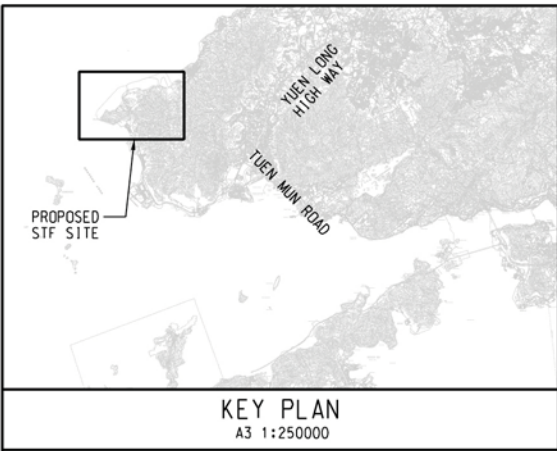

DEEP BAY

PROPOSED SLUDGE TREATMENT FACILITIES

EXISTING CLP ASH LAGOON AT TSANG TSUI

WENT LANDFILL

大水坑  
831250 N

TSANG KOK STREAM

BLACK POINT POWER STATION

BLACK POINT

URMSTON ROAD

配水庫  
Ser Res

龍鼓上棚  
Lung Au  
Sheung Tan

830000 N

807500 E

808750 E

810000 E

811250 E

DATE: GUOXH 2008-9-30

**MAUNSELL | AECOM**  
Metcalf & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)  
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY  
**LOCATION PLAN OF PROPOSED SLUDGE TREATMENT FACILITIES**

SCALE	A3 1:12500	DATE	SEP. 2008
CHECK	PPMY	DRAWN	XCF
JOB No.	60015756	DRAWING No.	FIGURE 1.1
		REV	-

---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---


**Figure 3.2**

**WENT Landfill Gas Control Zone**




SECTION OF NULLAH  
WHERE WATER IS ALWAYS  
PRESENT

INSET

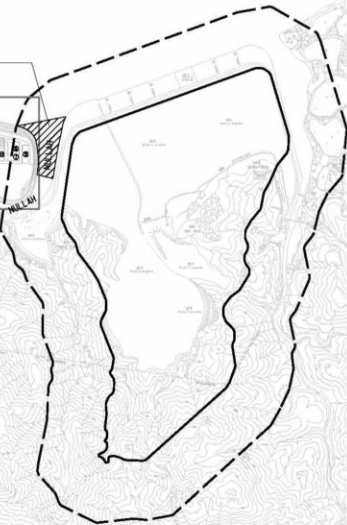

INSET



#### LEGEND

- ① DELIVERY BAY
- ② INCINERATORS AND AIR CONTROL EQUIPMENT
- ③ FUEL GAS RESIDUE SILOS, ASH SILOS & LOADING AREA
- ④ CHEMICAL / FUEL STORAGE AND FEEDING
- ⑤ STACK
- ⑥ ADMINISTRATION BUILDING & LABORATORY
- ⑦ MAINTENANCE WORKSHOP
- ⑧ UTILITY YARD
- ⑨ DESALINATION PLANT, SEAWATER PUMPING STATION & STORAGE TANK
- ⑩ SEWAGE TREATMENT WORKS

WENT LANDFILL  
CONSULTATION ZONE  
BOUNDARY

WENT LANDFILL  
WASTE BOUNDARY

DATE: 04/08

MAUNSELL | AECOM

Mansell & Gohy Ltd.

AGREEMENT NO. CE 28/2003 (EP)  
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY  
WENT LANDFILL CONSULTATION ZONE

SCALE	1:11000	DATE	APR. 2008
CHECK	TCYC	DRAWN	ALFA
DWG NO.	60039510	REVISION NO.	FIGURE 10.1
		REV	-



---

## FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,  
Fugro Development Centre,  
5 Lok Yi Street, 17 M.S. Castle Peak Road,  
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233  
Telefax : +852-2450 6138  
E-mail : [matlab@fugro.com.hk](mailto:matlab@fugro.com.hk)  
Website : [www.fugro.com](http://www.fugro.com)

**MaterialLab**

---

**Figure 4.1**

### **Ecological Transect Route**


0m 100m 200m 300m 400m



DEEP BAY

PROPOSED SLUDGE  
TREATMENT FACILITIES


EXISTING CLP ASH LAGOON  
AT TSANG TSUI

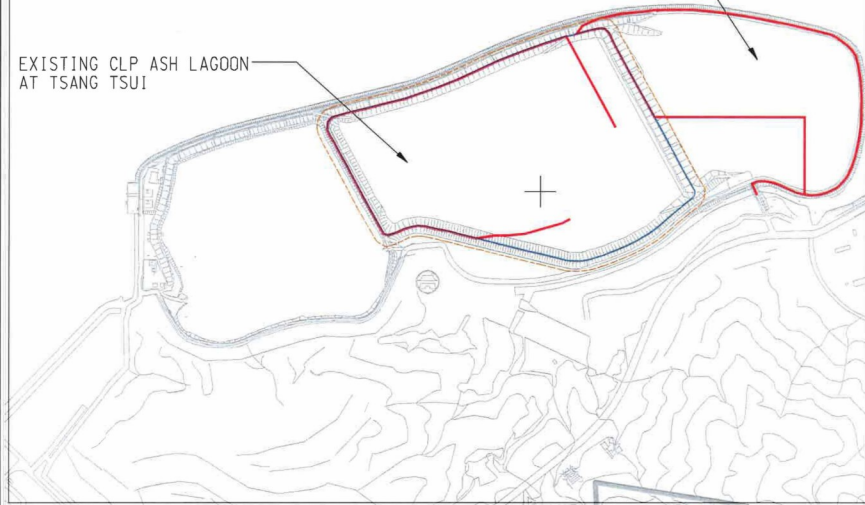

- Notes:
- Survey Route
  - Middle Lagoon Boundary
  - - - 20m from Middle Lagoon Boundary

 **Aale Ecological Consultants Ltd**

Project Title:  
**Contract No. EP/SP/58/08  
Sludge Treatment Facilities**



Drawing Title:  
**Ecological Transect Route**

Drawn: SK	Scale: As shown
Checked: DJS	Date: May 2011
Approved: DJS	File: --
Drawing Number: --	Revision: 1
