

Our ref.: CCL/MA13003/Corres/Out/vw150310_Mrpt1502

Environmental Protection Department
Environmental Assessment Division
Assessment and Noise Group
27th Floor, Southorn Centre,
130 Hennessy Road
Wan Chai, Hong Kong

By Courier

10 March 2015

Attn.: Mr. Tom TAM

Dear Sirs,

Environmental Permit (EP) No. FEP-24/004/1998/I
West Rail, Phase I - MTRC Works Contract 1117
Pat Heung Depot Modification Works


- Monthly Noise Monitoring Report (February 2015) for Pat Heung Depot Modification Works

On behalf of MTRCL, we are pleased to submit herewith three hard copies and one electronic copy of the captioned report in accordance with Condition 4.5 of the Project EP.

Please kindly note that the captioned report has been certified by the Environmental Team (ET) Leader and verified by the Independent Environmental Checker (IEC) as per Condition 4.5 of the Project EP.

Should you require any further information, please feel free to contact our Mr. Victor Wong at 2151-2078 or the undersigned at 2151 2089.

Yours faithfully,
Cinotech Consultants Ltd.



Dr. Priscilla Choy
Environmental Team Leader

Encl.

Cc. (all w/e)


EPD	(Attn: Mr. Wai CHAU)	w/encl.
MTRCL	(Attn: Mr. Richard KWAN)	w/o encl.
Paul Y	(Attn: Mr. Edmond Chan)	w/encl.

Paul Y. Construction Company, Limited

**MTR Works Contract 1117-
Pat Heung Depot Modification Works**

**Monthly Noise Monitoring Report
for
February 2015**

(Version 1.0)

Certified By 
Environmental Team Leader
(Dr. Priscilla Choy)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: info@cinotech.com.hk

MTR Corporation Limited

West Rail

Pat Heung Modification Works
Monthly Noise Monitoring Report No. 24
[Period from 1 to 28 February 2015]

(March 2015)

Verified by: Fredrick Leong 

Position: Independent Environmental Checker

Date: 10 Mar. 2015

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	1
Introduction	1
Summary of Construction Works undertaken during Reporting Period	1
Environmental Monitoring and Audit Progress	1
Noise.....	1
Waste Management	2
Environmental Site Inspection	2
Environmental Exceedance/Non-conformance/Complaint/Summon and Prosecution.....	2
Future Key Issues	2
1 INTRODUCTION	4
Purpose of the Report	4
Structure of the Report	4
2 PROJECT INFORMATION.....	5
Background	5
General Site Description	5
Construction Programme and Activities	5
Project Organisation	5
Status of Environmental Licences, Notification and Permits.....	6
Summary of EM&A Requirements	7
3 ENVIRONMENTAL MONITORING REQUIREMENTS.....	8
Construction Noise Monitoring.....	8
Monitoring Requirements.....	8
Monitoring Equipment	9
Monitoring Parameters, Frequency and Duration	9
Monitoring Methodology and QA/QC Procedures	9
4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	10
5 MONITORING RESULTS	11
Noise.....	11
Waste Management	11
6 ENVIRONMENTAL SITE INSPECTION.....	12
Site Audits	12
Implementation Status of Environmental Mitigation Measures.....	12
7 ENVIRONMENTAL NON-CONFORMANCE.....	14
Summary of Exceedances	14
Summary of Environmental Non-Compliance.....	14
Summary of Environmental Complaint	14
Summary of Environmental Summon and Successful Prosecution	14
8 FUTURE KEY ISSUES	15
Key Issues in the Coming Month	15
Monitoring Schedule for the Next Month	15
Construction Programme for the Next Month.....	15

9 CONCLUSIONS.....	16
Conclusions	16
Recommendations	16

LIST OF TABLES

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 2.1	Status of Environmental Licenses, Notification and Permits
Table 3.1	Construction Noise Monitoring Stations
Table 3.2	Criteria for Action and Limit Levels for Construction Noise
Table 3.3	Noise Monitoring Equipment
Table 3.4	Noise Monitoring Parameters, Frequency and Duration
Table 4.1	Status of Required Submissions under EP
Table 5.1	Quantities of Waste Generated from the Project
Table 6.1	Site Audit Observations

LIST OF FIGURES

Figure 1	Site Layout Plan
Figure 2	Project Organization Chart for Environmental Works
Figure 3	Location of Construction Noise Monitoring Stations

LIST OF APPENDICES

Appendix A	Tentative Construction Programme
Appendix B	Event and Action Plan
Appendix C	Copies of Calibration Certificates
Appendix D	Updated Environmental Mitigation Implementation Schedule
Appendix E	Environmental Monitoring Schedule
Appendix F	Noise Monitoring Results and Graphical Presentations
Appendix G	Waste Generation in the Reporting Month
Appendix H	Site Audit Summary
Appendix I	Summary of Exceedance
Appendix J	Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions

EXECUTIVE SUMMARY

Introduction

1. This is the 24th Monthly Noise Monitoring Report prepared by Cinotech Consultants Limited for MTR Works Contract 1117 - Pat Heung Depot (PHD) Modification Works. This report documents the findings of EM&A Works conducted from 1 February to 28 February 2015 since major construction works for Contract 1117 commenced on 1 March 2013.

Summary of Construction Works undertaken during Reporting Period

2. The major site activities undertaken in the reporting period include:
 - Site clearance and formation, site surveying
 - Auger piling, sheet-piling
 - embankment works, drainage works, manholes excavation
 - ELS works for P-way Workshop
 - RC substructure works and superstructural works for EMU extension building and IMB building
 - Modification works for protected corridor in existing EMU building
 - ABWF Works
 - Construction of retaining wall footing and permanent noise barrier at Location 3, Location 4 & Location 5
 - Hydroseeding.
3. As of this reporting period, there is no record of any project changes from that originally proposed as described in the latest Environmental Review Report (ERR) for this Works Contract 1117.

Environmental Monitoring and Audit Progress

4. A summary of the monitoring activities in this reporting period is listed below:
 - Construction Noise Monitoring during normal weekdays
 - NM1 4 times
 - NM2 4 times
 - NM3A 4 times
 - Environmental Site Inspection 4 times

Noise

5. 4 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations during normal weekdays of the reporting period. No exceedance was recorded during the reporting period.

Waste Management

6. Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. About 1,690 m³ of inert C&D materials were generated during the reporting period. Non-inert C&D wastes include 315 kg of paper/cardboard packaging materials and 58 m³ of general refuse were generated during the reporting period. The inert C&D materials generated from the Project were disposed of at TM 38 Area Fill Bank, while all non-inert waste was disposed of at NENT and WENT.

Environmental Site Inspection

7. A monthly joint environmental site inspection was carried out by the representatives of the Contractor, the IEC and the ET. Details of the audit findings and implementation status are presented in Section 6.

Environmental Exceedance/Non-conformance/Complaint/Summon and Prosecution

8. Summary of the events and action taken and key information in the reporting month is tabulated in **Table I** and **Table II** respectively.

Table I Summary Table for Events Recorded in the Reporting Month

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
Impact Noise Monitoring	0	0	N/A

Table II Summary Table for Key Information in the Reporting Month

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Notifications of any summons & prosecutions	0	---	N/A	N/A	---

Future Key Issues

9. Major site activities for the coming reporting month will include:
- Site clearance and formation, site surveying
 - sheet-piling
 - embankment works, drainage works, manholes excavation
 - ELS works for P-way Workshop
 - RC substructure works and superstructural works for EMU extension building and IMB building

- Modification works for protected corridor in existing EMU building
- ABWF Works
- Upgrading of existing noise barrier
- Construction of retaining wall footing and permanent noise barrier at Location 3 & Location 5
- Hydroseeding.

1 INTRODUCTION

- 1.1 Cinotech Consultants Limited (Cinotech) is commissioned by Paul Y. Construction Company, Limited as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme during construction phase of the MTR Works Contract 1117 –Pat Heung Depot (PHD) Modification Works (hereafter referred to “the Project”).

Purpose of the Report

- 1.2 This is the 24th Monthly Noise Monitoring Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 February to 28 February 2015 since major construction works for Contract 1117 commenced on 1 March 2013.

Structure of the Report

- 1.3 The structure of the report is as follows:

Section 1: **Introduction** - details the scope and structure of the report.

Section 2: **Project Information** - summarises background and scope of the project, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permits/Licenses during the reporting period.

Section 3: **Environmental Monitoring Requirement** - summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event / Action Plans, environmental mitigation measures as recommended in the Environmental Review Report (ERR) and relevant environmental requirements.

Section 4: **Implementation Status on Environmental Mitigation Measures** - summarises the implementation of environmental protection measures during the reporting period.

Section 5: **Monitoring Results** - summarises the monitoring results obtained in the reporting period.

Section 6: **Environmental Site Inspection** - summarises the audit findings of the weekly site inspections undertaken within the reporting period.

Section 7: **Environmental Non-conformance** - summarises any monitoring exceedance, environmental complaints and environmental summons within the reporting period.

Section 8: **Future Key Issues** - summarises the impact forecast and monitoring schedule for the next three months.

Section 9: **Conclusions and Recommendations**

2 PROJECT INFORMATION

Background

- 2.1 West Rail Line (WRL) is one of the strategic rail infrastructures in Hong Kong providing the people of Hong Kong an environmentally friendly and convenient way to travel between the western part of the New Territories and western Kowloon. Under the approved WRL Environmental Impact Assessment (EIA) Report (EIA-149/BC), it has a total length of about 30.5km with 9 stations, including Nam Cheong, Mei Foo, Tsuen Wan West, Kam Sheung Road, Yuen Long, Long Ping, Tin Shui Wai, Siu Hong, Tuen Mun and one depot at Pat Heung.
- 2.2 The EIA Report of WRL was prepared and submitted to Environmental Protection Department (EPD) prior to the enactment of the Environmental Impact Assessment Ordinance (EIAO) in 1998. Since the first Environmental Permit (EP) (EP-004/1998), there have been amendments made to the permit through a number of EP variation applications related to the main line of WRL.
- 2.3 This Works Contract 1117 covers the modification works at the existing Pat Heung Depot (PHD) of WRL to meet future operational and maintenance requirements. The PHD modification works include the construction of a new train wash plant, locomotive shed, permanent - way workshop, stabling sidings, extension of maintenance building and modification of noise barriers.
- 2.4 Since the modification works at PHD forms part of the WRL, a variation of environmental permit (VEP) was applied and a VEP (EP No. EP-004/1998/I) were subsequently granted. Moreover, a further Environmental Permit (FEP) (EP No: FEP-24/004/1998/I) on construction and operation of WRL (including the PHD modification works) was issued by Director of Environmental Protection (DEP) to the MTR Corporation Limited on 23 July 2012.

General Site Description

- 2.5 The site layout and proposed modification works are illustrated in **Figure 1**.

Construction Programme and Activities

- 2.6 A summary of the major construction activities undertaken in this reporting period is shown as follows. The tentative construction programme is presented in **Appendix A**.
- Site clearance and formation, site surveying
 - Auger piling, sheet-piling
 - embankment works, drainage works, manholes excavation
 - ELS works for P-way Workshop
 - RC substructure works and superstructural works for EMU extension building and IMB building
 - Modification works for protected corridor in existing EMU building
 - ABWF Works
 - Construction of retaining wall footing and permanent noise barrier at Location 3, Location 4 & Location 5
 - Hydroseeding.

Project Organisation

- 2.7 Different parties with different levels of involvement in the project organization include:
- Engineer or Engineer’s Representative (ER)– MTR Corporation (MTRC)
 - Contractor’s Environmental Team (Contractor’s ET) – Cinotech Consultants Ltd. (Cinotech)
 - Independent Environmental Checker (IEC) – Meinhardt Infrastructure and Environment Limited (MIEL)
 - Contractor – Paul Y. Construction Company, Limited(Paul Y)
- 2.8 The responsibilities of respective parties are detailed in Section 2 of the approved EM&A Programme for PHD Modification Works.
- 2.9 The project organisation including key personnel contact names and telephone numbers is presented in **Figure 2**.

Status of Environmental Licences, Notification and Permits

- 2.10 A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project is presented in **Table 2.1**.

Table 2.1 Status of Environmental Licenses, Notification and Permits

Permit / License No.	Valid Period		Status
	From	To	
Environmental Permit (EP)			
FEP-24/004/1998/J	21/10/2013	End of the Project	Valid
Notification pursuant to Air Pollution Control (Construction Dust) Regulation			
No.351534	26/10/2012	N/A	Valid
Billing Account for Construction Waste Disposal			
Account No. 7016256	2/11/2012	N/A	Valid
Registration of Chemical Waste Producer			
5218-531-P2991-02	4/12/2012	N/A	Valid
Effluent Discharge License under Water Pollution Control Ordinance (WPCO)			
WT00015378-2013	26/3/2013	31/3/2018	Valid
Construction Noise Permit			
GW-RN0514-14 (Area C: Location 4 Noise Barrier Upgrade)	13/9/2014	12/3/2015	Valid
GW-RN0546-14 (Area A: EMU Extension)	20/9/2014	19/3/2015	Valid
GW-RN0691-14 (Area C: OHL Footing near Tai Lam Tunnel)	11/11/2014	4/5/2014	Valid
GW-RN0003-15 (Area C: OHL Footing near to Kam Sheung Road Station)	12/1/2015	1/7/2015	Valid

Summary of EM&A Requirements

- 2.11 The EM&A programme under Works Contract 1117 require construction noise monitoring as well as environmental site audits. The EM&A requirements are described in the following sections, including:
- all monitoring parameters;
 - environmental quality performance limits (Action and Limit levels);
 - Event-Action Plans;
 - Environmental mitigation measures, as recommended in the Environmental Review Report (ERR) for the VEP (EP No. FEP-24/004/1998/I); and
 - Environmental requirements in contract documents.
- 2.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.
- 2.13 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely construction noise as well as audit works for the Project in the reporting month.

3 ENVIRONMENTAL MONITORING REQUIREMENTS

Construction Noise Monitoring

Monitoring Requirements

- 3.1 Noise monitoring was conducted in accordance with the approved EM&A Programme for PHD Modification Works.
- 3.2 With reference to the baseline monitoring report for the Project, **Table 3.1** and **Table 3.2** summarises the location of noise monitoring stations and shows the established Action and Limit Levels for construction noise monitoring works respectively. Location of the monitoring stations is shown on **Figure 3**.

Table 3.1 Construction Noise Monitoring Stations

ID in the approved EM&A Programme	ID in Baseline Noise Monitoring Report	Construction Noise Monitoring Station
NM1	NM1	Tourmaline Villa
NM2	NM2	Kam Po Road
NM3	NM3A ⁽¹⁾	Tai Kek Tsuen

Note:

- (1) Since permission of access could not be obtained, an alternative location at a village house just next to the original proposed monitoring location in the EM&A Programme was adopted for the baseline noise monitoring.

Table 3.2 Criteria for Action and Limit Levels for Construction Noise

Time Period ⁽¹⁾	Noise Monitoring Station	Action Level	Limit Level, dB (A)
0700-1900 hrs of normal weekdays	Tourmaline Villa (NM1)	When one documented valid complaint is received.	75.0
	Kam Po Road (NM2)		
	Tai Kek Tsuen (NM3A)		

Note:

- (1) If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority should be followed.

- 3.3 Should non-compliance of the criteria in **Table 3.2** occur, action in accordance with the Event and Action Plan in **Appendix B** should be carried out.

Monitoring Equipment

3.4 **Table 3.3** summarizes the noise monitoring equipment model being used.

Table 3.3 Noise Monitoring Equipment

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	Pulsar Instruments Model 93 (Serial no. B22369)	1
Calibrator	Pulsar Instruments Model 105 (Serial no. 60220)	1

Monitoring Parameters, Frequency and Duration

3.5 **Table 3.4** summarizes the monitoring parameters, frequency and total duration of monitoring.

Table 3.4 Noise Monitoring Parameters, Frequency and Duration

Station	Parameter	Period	Frequency
NM1, NM2 and NM3A	$L_{eq,30 \text{ min.}}^{(1)}$ (L_{10} and L_{90} were also recorded as supplementary information)	0700-1900 hours on normal weekdays	Once a week

Note (1): $L_{eq, 30 \text{ min.}}$ as six consecutive $L_{eq, 5 \text{ min}}$ readings.

Monitoring Methodology and QA/QC Procedures

Field Monitoring

3.6 The monitoring procedures are as follows:

- The microphone head of the sound level meter was positioned 1m exterior of the noise sensitive facade and lowered sufficiently so that the building's external wall acts as a reflecting surface.
- The battery condition was checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting : A
 - Time weighting : Fast
 - Measurement time : 5 minutes (obtaining six consecutive $L_{eq, 5 \text{ min}}$ readings for a $L_{eq, 30 \text{ min.}}$ reading)
- Prior to and after noise measurement, the meter was calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
- The wind speed at the monitoring station was checked with the portable wind meter. Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

- Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- At the end of the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- A façade correction of +3dB (A) shall be made to the noise parameter obtained by free field measurement.

Maintenance and Calibration

3.7 Maintenance and Calibration procedures were as follows:

- The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator were checked and calibrated at yearly intervals. Copies of calibration certificates are attached in **Appendix C**.

4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS

4.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the ERR, the Environmental Permit and approved EM&A Programme for PHD Modification Works. The status of submission required under the Environmental Permit is summarized in **Table 4.1**. The implementation status of the environmental mitigation measures during the reporting period is summarized in **Appendix D**.

Table 4.1 Status of Required Submissions under EP

EP Condition	Submission	Submission Date
Condition 4.5	Monthly Noise Monitoring Report (January 2015)	12 th February 2015

5 MONITORING RESULTS

Noise

- 5.1 In this reporting period, noise monitoring during non-restricted hours was conducted as scheduled at the designated locations. The noise monitoring schedule is shown in **Appendix E**.
- 5.2 The details of the monitoring results and graphical presentations are shown in **Appendix F**. The weather during the monitoring sessions was mainly cloudy and sunny.
- 5.3 Based on the on-site measurement, traffic on nearby major road is considered as a noise source other than construction works of the Project that affects the monitoring results of the reporting month.
- 5.4 No Action/Limit Level exceedance for construction noise monitoring was recorded in the reporting period.

Waste Management

- 5.5 Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials and dredging materials. Non-inert C&D materials are made up of general refuse, chemical waste, paper/cardboard packaging materials, plastic materials and metals. Metals generated from the project are also grouped into non-inert C&D materials as the metals were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in **Table 5.1**. The inert C&D materials and general refuse generated from the Project were disposed of at TM 38 Area Fill Bank, TKO 137 Area Fill Bank, WENT and NENT respectively. 315 kg of paper/cardboard packaging materials were generated during the reporting period. Detail of waste management data is presented in **Appendix G**.

Table 5.1 Quantities of Waste Generated from the Project

Reporting Month	Quantity					
	C&D Materials (inert) ^(a)	C&D Materials (non-inert) ^(b)				
		General Refuse	Chemical Waste	Paper/cardboard	Plastics	Metals
February 2015	1,690 m ³	58 m ³	0 kg	315 kg	0 kg	0 kg
Notes:						
(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.						
(b) Non-inert C&D materials include steel, paper/cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials.						

6 ENVIRONMENTAL SITE INSPECTION

Site Audits

- 6.1 Site audits were carried out by ET on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix H**.
- 6.2 Site audits were conducted on 3, 11, 16 and 24 February 2015 by ET. A joint site audit with the representative with IEC, ER, the Contractor and the ET was carried out on 16 February 2015. No site inspection was conducted by EPD during the reporting period. The details of observations during site audit can refer to **Table 6.1**.

Implementation Status of Environmental Mitigation Measures

- 6.3 According to the ERR, Environmental Permit and the approved EM&A Programme of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix D**.
- 6.4 During site inspections in the reporting period, no non-conformance was identified. The observations made during the audit sessions are summarized in **Table 6.1**.

Table 6.1 Site Audit Observations

Parameters	Date	Observations	Follow-up
<i>Water Quality</i>	30 December 2014	Sludge was observed in the sedimentation tank (Area A) and drainage channel (Area C, Location 3); Cement wash water should be retained on site or treated properly before discharging in Area C.	The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015. The accumulated sediment and muddy water identified in the u-channel in Area C (Location 3) has been cleared on 16 February 2015.
	6 January 2015	Accumulated sludge is observed in the drainage channel and sedimentation tank (Area A and C); The observed standing water in Area A u-channel should be filtered before discharging.	The accumulated sediment identified in the u-channel in Area C (Location 3) has been cleared on 16 February 2015. The discharge water quality in the drainage channel (Area A, near Option 1) has been improved on 27 January 2015; The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015.
	14 January 2015	Muddy water was observed in the u-channel in Area A, additional sand bags should be provided; Sludge in the sedimentation tank should be removed to improve discharge quality (Area A).	The discharge water quality in the drainage channel (Area A, near Option 1) has been improved on 27 January 2015; The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015.
	20 January 2015	Muddy water is observed in the drainage channel, additional sand bags should be placed along the	The discharge water quality in the drainage channel (Area A, near Option 1) has been improved on 27 January

Parameters	Date	Observations	Follow-up
		channel and more filtering facilities should be provided; Sedimentation tank should be maintained regularly by removing accumulated sludge (Area A).	2015; The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015.
	20 January 2015	<u>Reminder:</u> Accumulated sediment in the u-channel should be cleared (Area C, A 100).	The u-channel has been maintained and provided with sand bag bunding on 16 February 2015.
	27 January 2015	Discharge water quality from the sedimentation tank should be improved by adjusting the discharge rate and chemical dosage (Area A); Oil stain in the u-channel (near S18) should be cleared.	The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015.
	3 February 2015	Sediment and general refuse in the sedimentation tank should be cleared to maintain the discharge water quality (Area A); Muddy water is observed in the drainage channels, access to the channels should be blocked to prevent road wash water from entering (Area C, A 100, near Area D)	The discharge water quality from the sedimentation tank in Area A has been improved on 11 February 2015. ; New sand bags were provided to the drainage channel in Area C on 16 February 2015.
	3 February 2015	<u>Reminder:</u> The u-channel near S-18 should be maintained by clearing any accumulated oil stain (Area A).	The identified oil stain has been cleared on 11 February 2015.
	11 February 2015	Oil observed in the u-channel should be cleared; The sand bags in the u-channel should be replaced and provided with oil absorbent materials (Area A, near Option 1).	The water quality was observed to be improved and new sand bags were provided on 16 February 2015.
	16 February 2015	Cloudy water is observed in the sedimentation tank (Area A); discharge water quality in Area A should be improved by adjusting the chemical dosage of the tank.	The item was found outstanding on 24 February 2015; Follow-up status will be provided in the next reporting month.
	24 February 2015	<u>Reminder:</u> The Contractor is reminded to clear the accumulated mud and other waste in the u-channel regularly (Area C, A100).	Follow-up status will be provided in the next reporting month.
<i>Noise</i>	N/A	N/A	N/A
<i>Tree Protection/ Landscape and Visual</i>	N/A	N/A	N/A

Parameters	Date	Observations	Follow-up
<i>Air Quality</i>	16 February 2015	<u>Reminder:</u> Black smoke emission is observed from the excavator in Area B.	Excessive smoke emission was not observed from the excavators in Area B.
<i>Waste / Chemical Management</i>	27 January 2015	Adequate drip tray should be provided to the containers (Area A).	The identified containers were observed to be contained by drip tray on 16 February 2015.
	3 February 2015	Containers should be provided with drip tray (Area A).	The identified containers were observed to be contained by drip tray on 16 February 2015.
	16 February 2015	<u>Reminder:</u> General refuse and other waste should be stored in designated containers and removed regularly (Area C and D).	Container has been provided to store the disposed waste in Area D on 24 February 2015; No major general refuse accumulation was observed in Area C on 3 March 2015.
	24 February 2015	<u>Reminder:</u> Construction equipment and materials should be stored properly in the identified area (Area B).	Follow-up status will be provided in the next reporting month.
<i>Permits/ Licenses</i>	N/A	N/A	N/A

7 ENVIRONMENTAL NON-CONFORMANCE

Summary of Exceedances

- 7.1 No exceedance of monitoring results was recorded in the reporting period. The summary of exceedance is provided in **Appendix I**.

Summary of Environmental Non-Compliance

- 7.2 No environmental non-compliance was recorded in the reporting period.

Summary of Environmental Complaint

- 7.3 No environmental Project-related complaint was received in the reporting month. The Cumulative Complaint Log since the commencement of the Project is presented in **Appendix J**.

Summary of Environmental Summon and Successful Prosecution

- 7.4 There was no successful environmental prosecution or notification of summons received since the Project commencement. The Cumulative Log for environmental summon and successful prosecution since the commencement of the Project is presented in **Appendix J**.

FUTURE KEY ISSUES

Key Issues in the Coming Month

7.5 Key issues to be considered in the coming month include:

- Handling of waste water arising from drilling works and surface run-off;
- Dust control during loading of materials and excavation;
- Oil leakage from equipment;
- Noise nuisance generated by on-site construction and demolition works; and
- Protection of retained trees within construction site.
- Maintaining the sand bags and bundings at the u-channel to prevent muddy run-off from directly accessing the main drainage channels.

Monitoring Schedule for the Next Month

7.6 The tentative construction noise monitoring schedule for the next month is shown in **Appendix E**.

Construction Programme for the Next Month

7.7 A tentative construction programme is provided in **Appendix A**. The major construction activities in the coming month will include:

- Site clearance and formation, site surveying
- sheet-piling
- embankment works, drainage works, manholes excavation
- ELS works for P-way Workshop
- RC substructure works and superstructural works for EMU extension building and IMB building
- Modification works for protected corridor in existing EMU building
- ABWF Works
- Upgrading of existing noise barrier
- Construction of retaining wall footing and permanent noise barrier at Location 3 & Location 5
- Hydroseeding.

9 CONCLUSIONS

Conclusions

- 8.1 This Monthly Noise Monitoring Report presents the EM&A works undertaken during the period from 1 February to 28 February 2015 since major construction works for Contract 1117 commenced on 1 March 2013 in accordance with approved EM&A Programme for PHD Modification Works and the requirement under FEP-24/004/1998/I.
- 8.2 As of this reporting period, there is no record of any project changes from that originally proposed as described in the latest Environmental Review Report (ERR) for this Works Contract 1117.
- 8.3 No exceedance of monitoring results was recorded in the reporting period.
- 8.4 There was no environmental complaint, prosecution or notification of summons received.
- 8.5 The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Recommendations

- 8.6 The following recommendations were made for the next reporting month during the site audit to the Contractor:

Water Quality

- Sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all time;
- Bunding should be provided to confine the runoff in site area, particularly along the drainage channel;
- U-channel should be maintained by regularly remove trapped mud and provide coverage and sediment baffles to the channel wherever possible;
- The discharge quality must meet the requirements specified in the discharge licence.


Waste/Chemical Management

- Good site practice of providing drip trays for temporary use of chemicals is recommended to sustain. Drip trays should be properly maintained; and
- Proper maintenance should be provided to equipment in site to prevent oil leakage.
- Oil stains on the floor should be treated as chemical waste and cleaned off immediately.

Air Quality


- Proper covering of stockpile, especially cement, should be provided to reduce dust generation; and
- Adequate water spraying should be applied on the haul roads and site entrances to reduce dust emission generated by traffic movement.

FIGURES

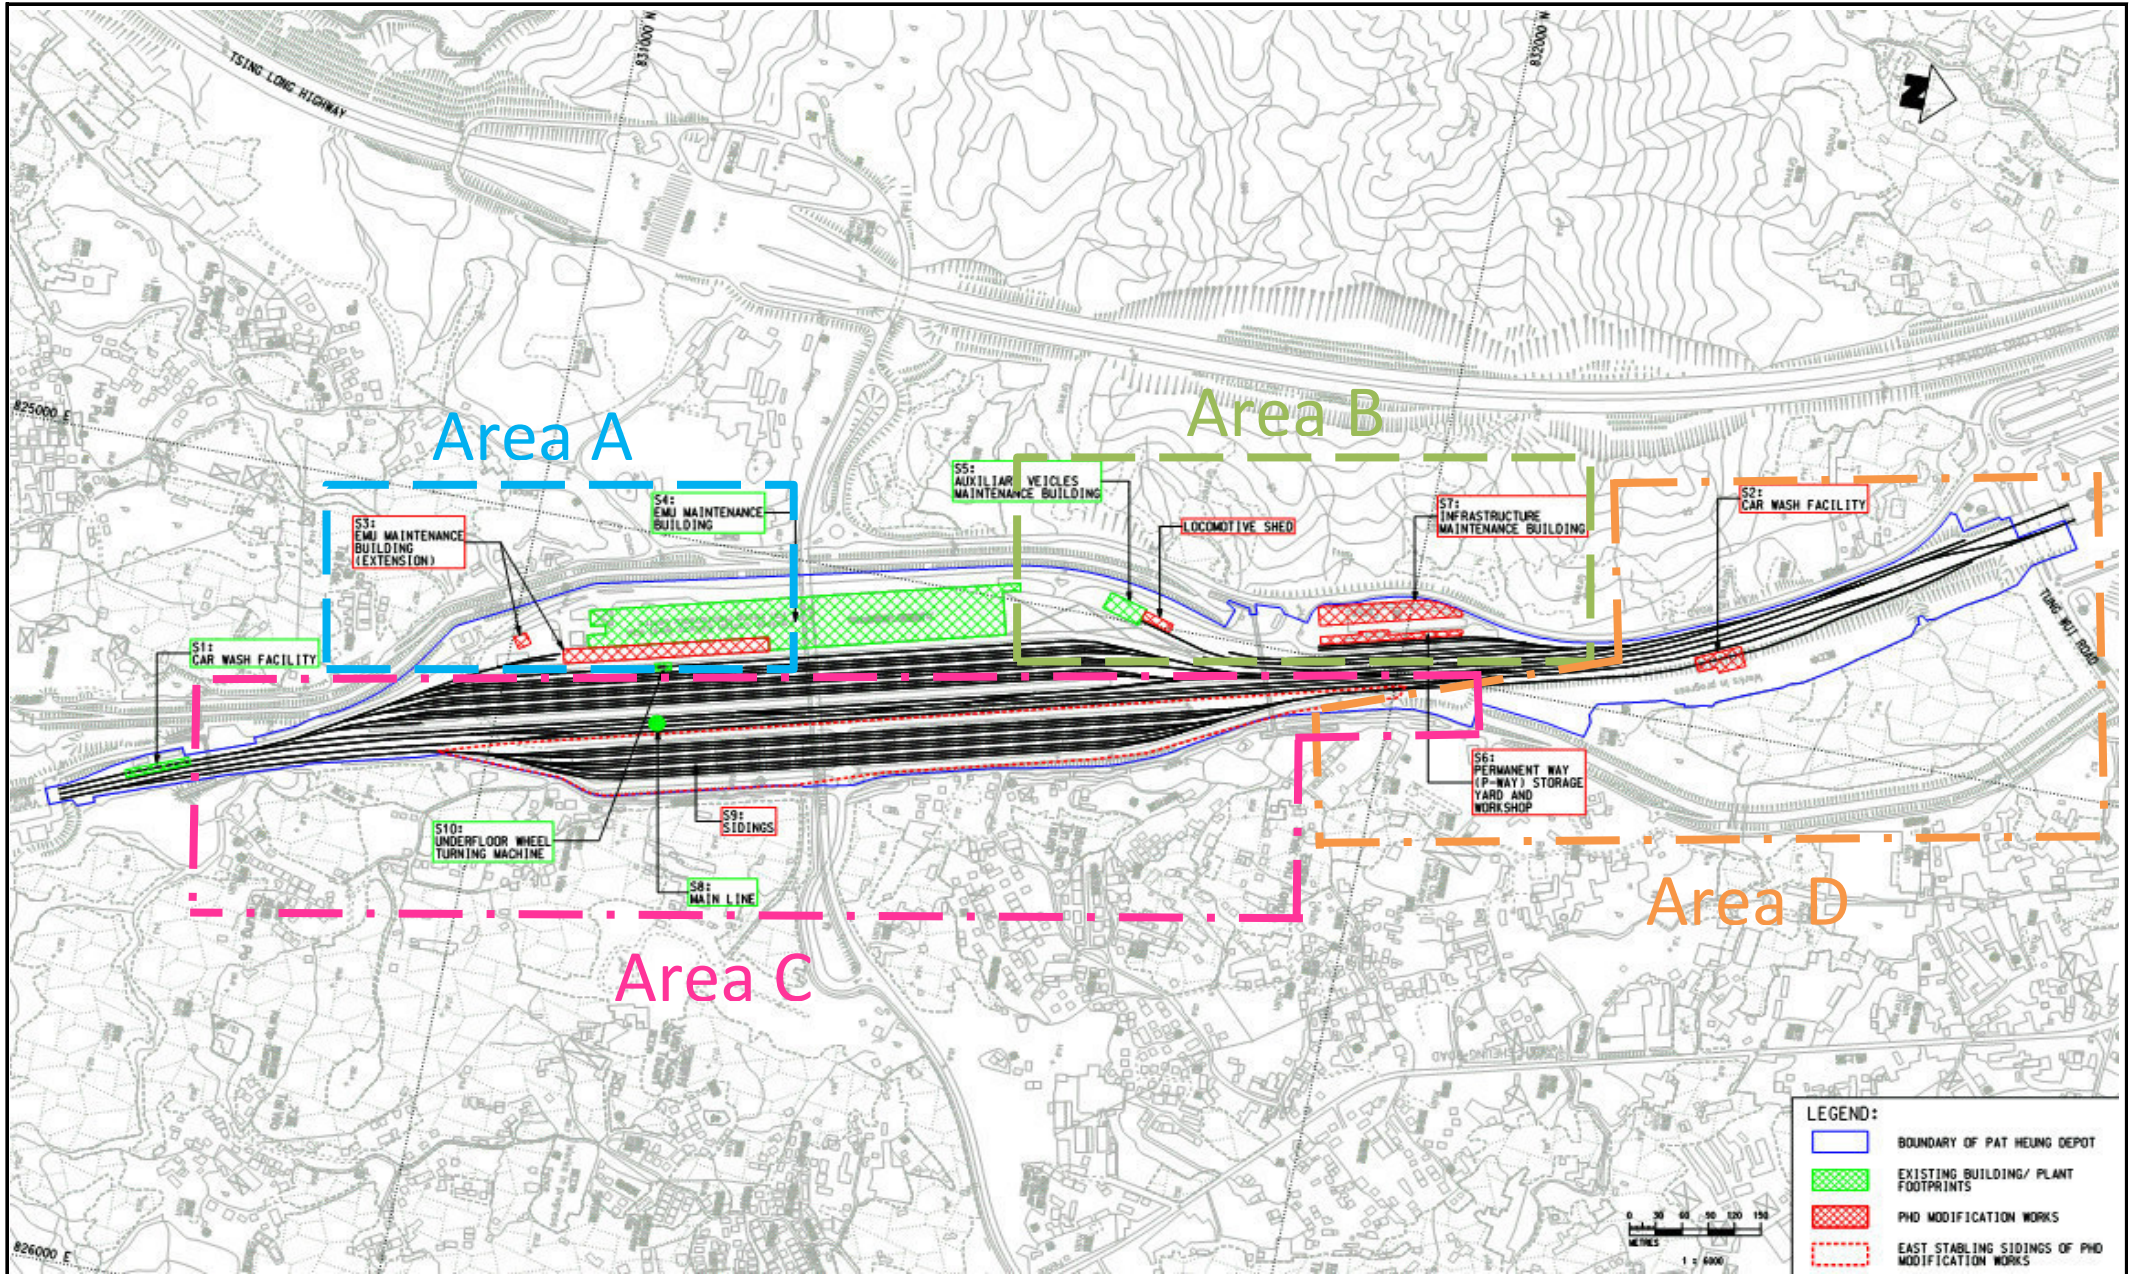


Title	SCL Contract 1117 Shatin to Central Link - Pat Heung Depot Modification Works		Scale	N.T.S	Proposal	MA13003
	Site Layout Plan		Date	Apr-13	Figure	



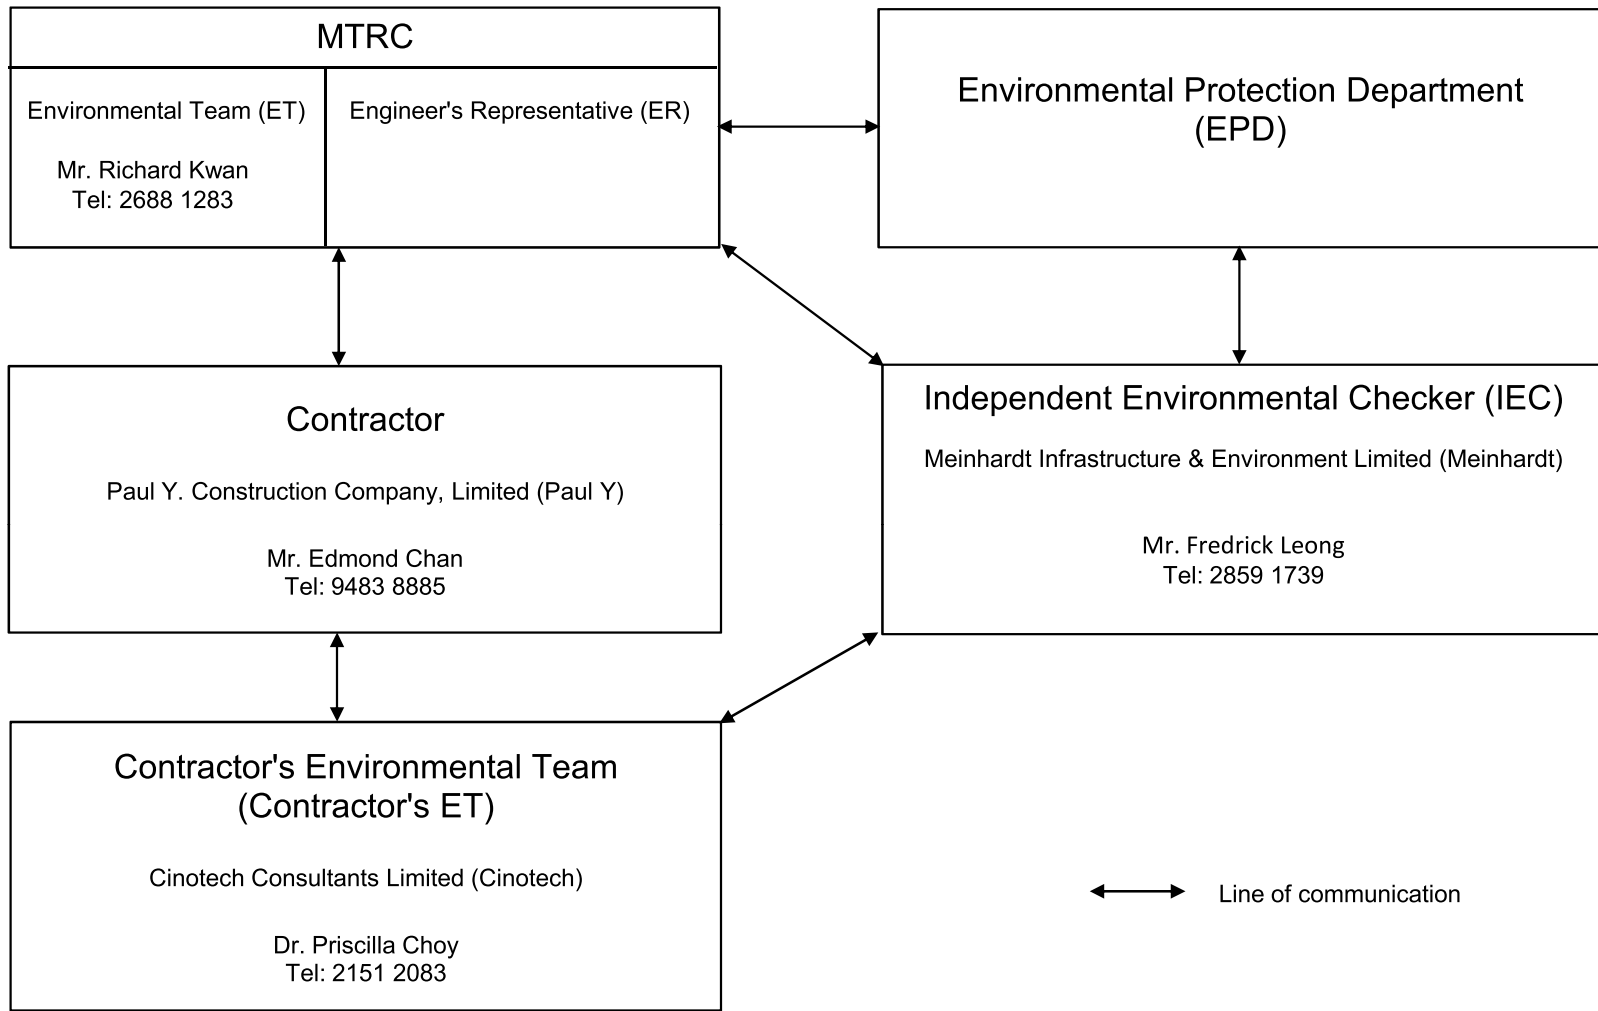

←→ Line of communication

Title	SCL Contract 1117		Scale	Propose	CINOTECH
	Shatin to Central Link - Pat Heung Depot Modification Works		N.T.S	No. MA13003	
Project Organisation Chart for Environmental Works			Date	Figure	
			Aug-13	2	

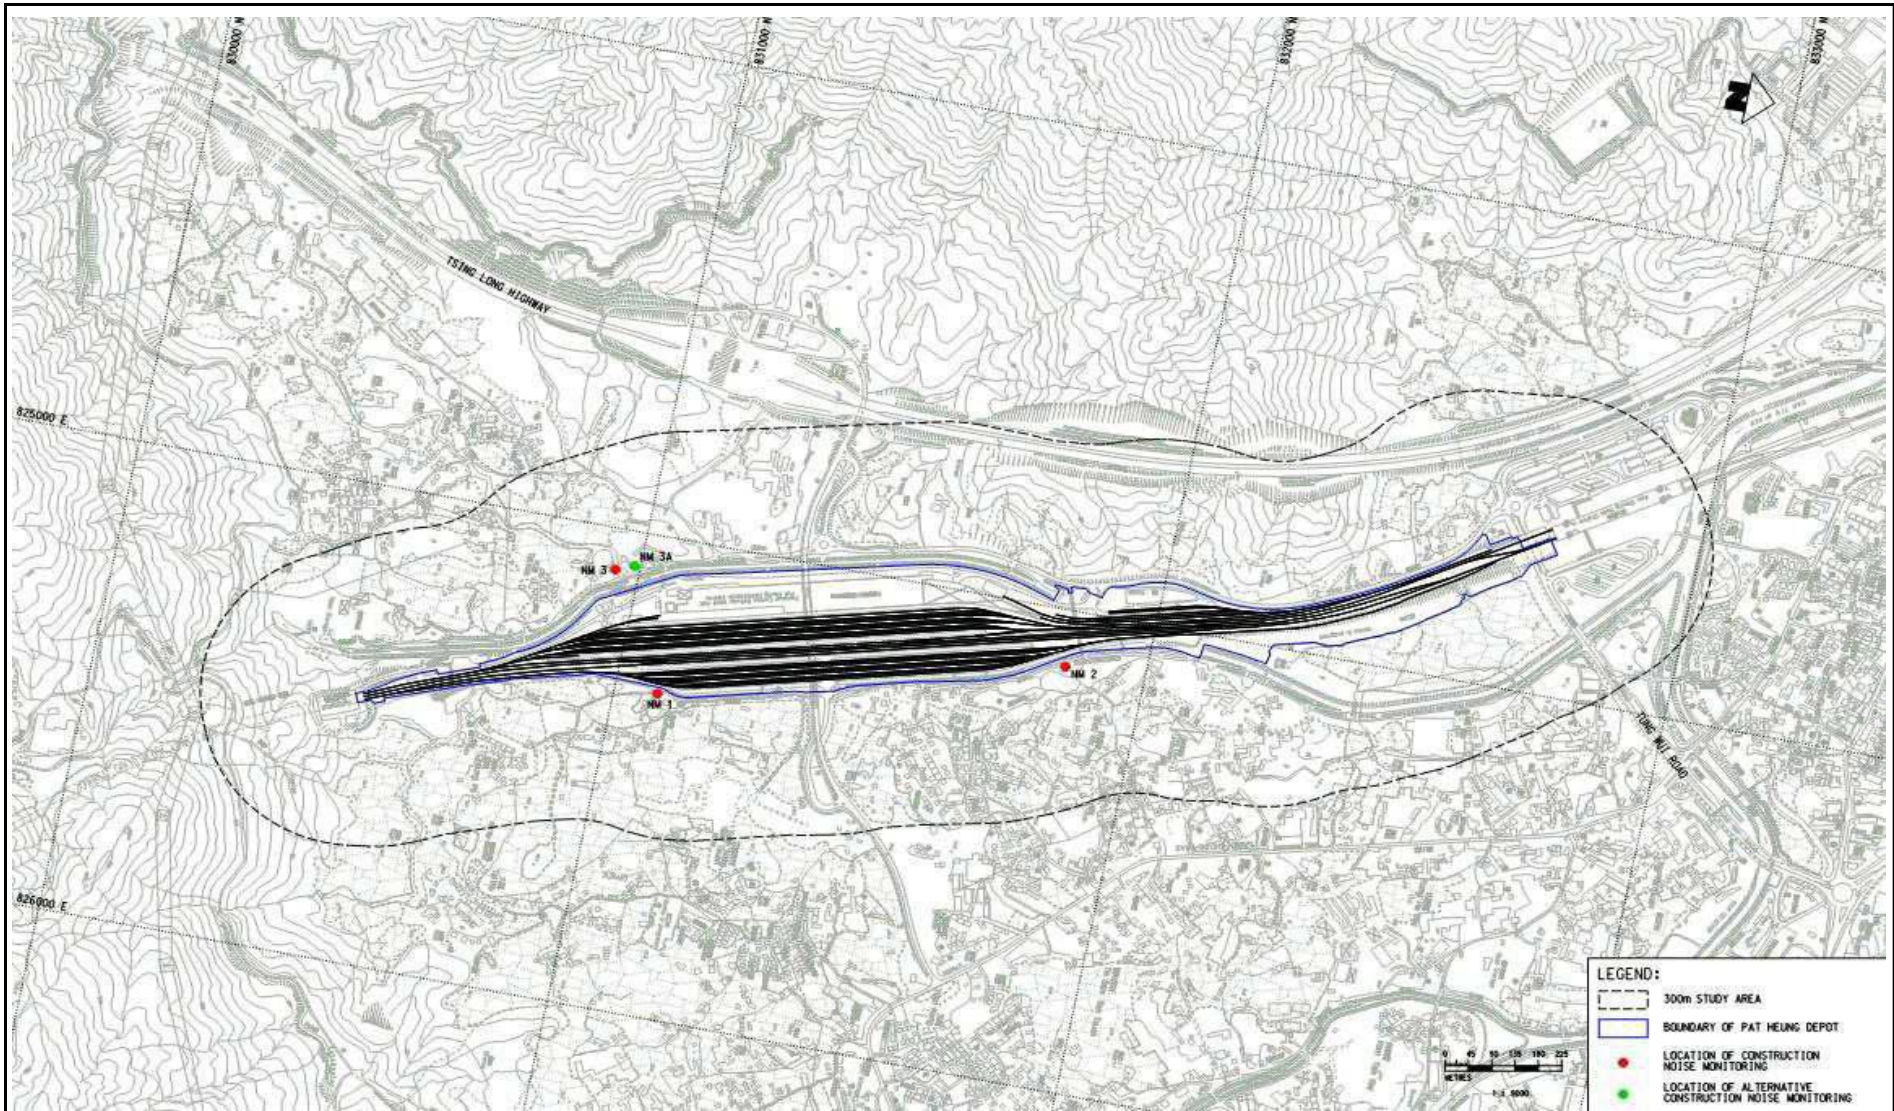


Title	MTR Works Contract 1117 Pat Heung Depot Modification Works		Scale	N.T.S	Proposal No.	MA13003	CINOTECH
	Location of Constrction Noise Monitoring Stations		Date	Apr-13	Figure	3	

**APPENDIX A
TENTATIVE CONSTRUCTION
PROGRAMME**

SCL 1117 Pat Heung Depot Modification Works

04-Dec-13

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	Late Start	Late Finish	Total Float	2013												2014												2015												2016											
									D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	D	J	F	A						
Area B - New Fuel Station - Works Area W5A		95	12	01-Mar-13 A	13-Aug-13	27-Jul-13	25-Sep-13	36																																																
Demolition		6	0	30-Mar-13 A	06-Apr-13 A	27-Jul-13	27-Jul-13																																																	
Hoarding Erection (Stage 1)		6	0	12-Mar-13 A	28-Mar-13 A	27-Jul-13	27-Jul-13																																																	
E0 - Geotechnical Instrumentation and Monitoring		12	0	01-Mar-13 A	14-Mar-13 A	27-Jul-13	27-Jul-13																																																	
E1 - Excavation and Foundation		9	0	06-Apr-13 A	23-Apr-13 A	27-Jul-13	27-Jul-13																																																	
E2 - Civil & Structures Works		43	0	24-Apr-13 A	31-Jul-13 A	27-Jul-13	27-Jul-13																																																	
E4 - BS Installation Works		40	0	01-Jun-13 A	11-Jul-13 A	27-Jul-13	27-Jul-13																																																	
Interfacing Coordination (Area B)		14	14	31-Jul-13	13-Aug-13	12-Sep-13	25-Sep-13	43																																																
Area B - AVM Building - Works Area W5B		170	170	17-Aug-13	13-Mar-14	16-Dec-13	30-Mar-14	14																																																
ABWF Works (AVMB Building) (Area B)		48	48	17-Aug-13	15-Oct-13	16-Dec-13	15-Feb-14	100																																																
BS Installation Works (AVMB Building) (Area B)		36	36	28-Jan-14	13-Mar-14	17-Feb-14	30-Mar-14	14																																																
Area B - Infrastructure Maintenance Building (IMB)		699	665	22-Apr-13 A	27-Oct-15	17-Sep-13	28-Nov-15	28																																																
E1 - Excavation and Foundation		268	234	22-Apr-13 A	16-May-14	17-Sep-13	05-Jul-14	41																																																
E2 - Civil & Structures Works		162	162	17-May-14	27-Nov-14	07-Jul-14	17-Jan-15	41																																																
E3 - ABWF Works		220	220	28-Nov-14	27-Aug-15	02-Feb-15	31-Oct-15	53																																																
E4 - BS Installation Works		220	220	28-Nov-14	27-Aug-15	19-Jan-15	31-Oct-15	53																																																
Transformer Room at IMB		252	252	20-Jun-14	25-Apr-15	17-Oct-14	26-Apr-15	0																																																
Lift Shaft at IMB		329	329	17-Sep-14	27-Oct-15	30-Apr-15	28-Nov-15	28																																																
Area B - Permanent Way (P-Way) Workshop		659	659	15-Jul-13 A	20-Oct-15	14-Aug-13	31-Oct-15	10																																																
E1 - Excavation and Foundation		134	134	04-Aug-14	14-Jan-15	14-Aug-14	24-Jan-15	10																																																
E2 - Civil & Structures Works		54	54	14-Jan-15	21-Mar-15	26-Jan-15	01-Apr-15	10																																																
E3 - ABWF Works		88	88	21-Mar-15	11-Jul-15	02-Apr-15	31-Oct-15	94																																																
E4 - BS Installation Works		172	172	21-Mar-15	20-Oct-15	16-Apr-15	31-Oct-15	10																																																
E5 - Associated Works		299	299	15-Jul-13 A	02-Aug-14	14-Aug-13	14-Aug-14	10																																																
Area B - New Loco Shed - Works Area W5C		298	298	25-Jul-13 A	01-Aug-14	17-Sep-13	27-Sep-14	48																																																
E1 - Excavation and Foundation		110	110	25-Jul-13 A	09-Dec-13	17-Sep-13	20-Dec-13	10																																																
E2 - Civil & Structures Works		48	48	19-Oct-13	13-Dec-13	26-Oct-13	20-Dec-13	6																																																
E3 - ABWF Works		82	82	14-Dec-13	26-Mar-14	21-Dec-13	09-Jun-14	57																																																
E4 - BS Installation Works		156	156	20-Jan-14	01-Aug-14	03-Feb-14	27-Sep-14	48																																																
Interfacing Coordination (Loco Shed)		0	0	18-Jan-14	18-Jan-14	25-Jan-14	25-Jan-14	6																																																
New Training Track		104	67	17-Jun-13 A	21-Oct-13	31-Jul-13	21-Oct-13	0																																																
New Training Track - Works Area W6A (Area B)		104	67	17-Jun-13 A	21-Oct-13	31-Jul-13	21-Oct-13	0																																																
Miscellaneous and External Works (Overhead Crane)		424	424	18-Dec-13	30-May-15	23-Dec-13	25-Jul-15	47																																																
Overhead Crane - Works Area W6/W6B/W6D		424	424	18-Dec-13	30-May-15	23-Dec-13	25-Jul-15	47																																																
Area C - East Stabling/Extg Loco Shed/Noise Barrier 3 & 4/Extg A100 Road		588	514	22-Oct-12 A	27-Apr-15	31-Jul-13	25-Sep-15	126																																																
Preliminary Works Submission (Area C)		314	240	03-Dec-12 A	23-May-14	31-Jul-13	29-Aug-14	82																																																
Materials Procurement (Area C)		35	0	22-Oct-12 A	31-Dec-12 A	31-Jul-13	02-Aug-13																																																	
Materials Submission (Area C)		24	5	17-Jun-13 A	05-Aug-13	28-Aug-13	02-Sep-13	24																																																
Site Construction Works (Area C)		588	514	21-Nov-12 A	27-Apr-15	31-Jul-13	25-Sep-15	126																																																
Site Preparation Works (Works Areas W11, W12, W13, W3a & W3b)		360	286	21-Nov-12 A	18-Jul-14	31-Jul-13	05-Aug-14	15																																																
Demolition		360	286	21-Nov-12 A	18-Jul-14	31-Jul-13	05-Aug-14	15																																																
General Site Clearance		48	0	28-Dec-12 A	27-Feb-13 A	31-Jul-13	31-Jul-13																																																	
Area C - Existing Loco Shed		24	24	02-Aug-14	29-Aug-14	30-Aug-14	27-Sep-14	24																																																
Demolition		24	24	02-Aug-14	29-Aug-14	30-Aug-14	27-Sep-14	24																																																
Miscellaneous and External Works (Pipe Jacking Works)		269	268	17-Jun-13 A	27-Jun-14	02-Aug-13	29-Jun-14	1																																																

 保華建築有限公司 Paul Y. Construction Company, Limited	■ Remaining Level of Effort ■ Actual Work ■ Remaining Work	■ Critical Remaining Work ◆ Milestone	Revised Construction Programme (CP04Frev1) Page 2 of 3 06-Sep-14	SCL 1117 Pat Heung Depot Modification Works			
	Date 04-Dec-13	Revision CP04Frev1 (updated ver...)	Che...	Ap...	

APPENDIX B
EVENT AND ACTION PLAN

Event and Action Plan for Noise Monitoring during Construction Phase

Event	Action			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IEC, Contactor, and ER; 2. Discuss with the ER, IEC, and Contractor on remedial measures required; and 3. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the contractor; and 2. Review and advise the ET and ER on the effectiveness of the remedial measures proposed by the Contractor. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor, IEC and ET; 3. Review and agree on the remedial measures proposed by the Contractor; and 4. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Investigate the complaint and propose remedial measures; 2. Report the results of investigation to the IEC, ET and ER; 3. Submit noise mitigation proposals to ER with copy to the IEC and ET within 3 working days of notification; and 4. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Notify IEC, EPD and Contractor; 2. Repeat measurement to confirm findings; 3. Increase monitoring frequency; 4. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 5. Arrange meeting with the IEC, Contractor and ER to discuss the remedial measures to be taken; 6. Inform IEC, ER, EPD the causes and actions taken for the exceedances; and 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET; 2. Check the Contractor's working method; 3. Discuss with the ER, ET, and Contractor on the potential remedial measures; and 4. Review and advise the ET and ER on the effectiveness of the remedial measures proposed by the Contractor. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor, IEC and ET; 3. In consultation with the ER and IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source and investigate the causes of exceedance; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER with copy to IEC and ET within 3 working days; 4. Implement the agreed proposals; 5. Revise and resubmit proposals if problem still not under control; and 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated

**APPENDIX C
COPIES OF CALIBRATION
CERTIFICATES**



华南国家计量测试中心
广东省计量科学研究院

SOUTH CHINA NATIONAL CENTER OF METROLOGY
GUANGDONG INSTITUTE OF METROLOGY



校准证书

CALIBRATION CERTIFICATE

证书编号 SSD201406950
Certificate No.

第 1 页, 共 6 页
Page of

委托方 Paul Y Construction Co. Ltd
Client

委托方地址
Add. of Client

计量器具名称 Sound Level Meter
Description

型号规格 93
Model/Type

制造厂 Pulsar
Manufacturer

出厂编号 B22369
Serial No.

设备编号
Equipment No.

接收日期 2014 年 12 月 15 日
Date of Receipt Y M D

结论 符合JJG 188-2002中1级技术要求
Conclusion

校准日期 2014 年 12 月 17 日
Date of Calibration Y M D

批准人
Approved Signatory

核 验
Inspected by

校 准
Calibrated by

证书专用章
Stamp



本中心地址: 中国广州市广园中路松柏东街30号 邮政编码: 510405
电话: (8620)86594172 传真: (8620)86590743 投诉电话: (8620)26296063 E-mail: scm@scm.com.cn
Add: No.30, Songbaidong Street, Guangyuanzhong Road, Guangzhou, P. R. China
Post Code: 510405 Tel: (8620)86594172 Fax: (8620)86590743 Complaint Tel: (8620)26296063
证书真伪查询: www.scm.com.cn; www.mtsp.com Certificate AuthenticityIdentify: www.scm.com.cn; www.mtsp.com



说 明

证书编号 SSD201406950
Certificate No.

DIRECTIONS

第 2 页, 共 6 页
Page of

1. 本中心是国家质量监督检验检疫总局在华南地区设立的国家法定计量检定机构, 计量授权证书号是: (国) 法计 (2012) 01043号、(国) 法计 (2012) 01032号。本中心质量管理体系符合 ISO/IEC 17025:2005 标准的要求。

This laboratory is the National Legal Metrological Verification Institution in southern China set up by the General Administration of Quality Supervision, Inspection and Quarantine of the People's Republic of China (AQSIQ) under authorization certificates No.(2012)01043 & (2012)01032. The quality system is in accordance with ISO/IEC 17025:2005.

2. 本中心所出具的数据均可溯源至国家计量基准和国际单位制(SI)。

All data issued by this laboratory are traceable to national primary standards and International System of Units (SI).

3. 本次校准的技术依据:

Reference documents for the calibration:

JJG 188-2002 声级计检定规程 V. R. of Sound Level Meters

4. 本次校准所使用的主要计量标准器具:

Major standards of measurement used in the calibration:

设备名称/型号 Name of Equipment /Model	编号 Serial No.	证书号/有效期 Certificate No. /Due Date	计量特性 Metrological Characteristic
标准传声器 Standard Microphones /4180	2488312	LSae2014-1017 /2015-04-13	声压灵敏度 级: 0.05dB~0.12dB (k=2) Sound pressure sensitivity level: 0.05dB~0.12dB (k=2)
消音箱 Sound Reducing Enclosure /2.0 m×1.4 m×1.4 m	1	SSD201402646 /2015-05-26	允差: ±1.5 dB MPE: ±1.5 dB
PULSE分析系统 Pulse analyzer System /3560C (3110模块)	2392397	SSD201402188 /2015-04-24	电平: $U_{rel}=0.1\%$, 频 率: $U_{rel}=0.001\%$ (k=2) Voltage: $U_{rel}=0.1\%$, Frequency : $U_{rel}=0.001\%$ (k=2)

5. 校准地点、环境条件:

Place and environmental conditions of the calibration:

地点	声学/振动实验室	温度	(23±3) °C	相对湿度	(40~50) %
Place	Acoustics/Vibration Lab.	Temperature		R.H.	

6. 被校准仪器限制使用条件:

Limiting condition of the instrument calibrated:

注: 1. 本证书校准结果只与受校准仪器有关。

2. 未经本机构书面批准, 不得部分复制此证书。

Note: 1. The results relate only to the items calibrated.

2. This certificate shall not be reproduced except in full, without the written approval of our laboratory.



校准结果

RESULTS OF CALIBRATION

证书编号: SSD201406950
Certification No.

原始记录编号: 2201406950
Record No.

第 3 页, 共 6 页
Page of

1 外观: 合格

Apparent inspection: Pass

2 声级计指示声级调整:

Level Calibration

(声校准器型号: 4231

标准声压级: 94.0 dB)

Sound Level Calibrator Type

Standard level

校准前示值: 93.7 dB

校准后示值: 94.0 dB

传声器型号/编号: UK224/20042221

Indication before Calibrated

Indication after Adjusted

Microphone type/serial number

3 频率计权: 见表1、表2、表3

Frequency weightings: Showed in table 1、table2、table 3

表1 Table 1

标称频率 (Hz)	实测值A计权 (dB)	允许范围 (dB)	结论
Nominal frequency	Measured Value A-weighting	Tolerance	Conclusion
10	-67.5	$-\infty \sim -66.9$	合格(Pass)
20	-50.2	$-53.0 \sim -48.0$	合格(Pass)
31.5	-39.6	$-41.4 \sim -37.4$	合格(Pass)
63	-26.4	$-27.7 \sim -24.7$	合格(Pass)
125	-15.9	$-17.6 \sim -14.6$	合格(Pass)
250	-8.5	$-10.0 \sim -7.2$	合格(Pass)
500	-3.2	$-4.6 \sim -1.8$	合格(Pass)
1000(ref.)	0.0	$-1.1 \sim +1.1$	合格(Pass)
2000	+1.2	$-0.4 \sim +2.8$	合格(Pass)
4000	+0.9	$-0.6 \sim +2.6$	合格(Pass)
8000	-1.2	$-4.2 \sim +1.0$	合格(Pass)
16000	-6.1	$-23.6 \sim -3.1$	合格(Pass)
20000	-8.5	$-\infty \sim -5.3$	合格(Pass)



校准结果

RESULTS OF CALIBRATION

证书编号: SSD201406950
Certification No.

原始记录编号: 2201406950
Record No.

第 4 页, 共 6 页
Page of

表2 Table 2

标称频率 (Hz)	实测值C计权 (dB)	允许范围 (dB)	结论
Nominal frequency	Measured Value C-weighting	Tolerance	Conclusion
10	-14.5	$-\infty \sim -10.8$	合格(Pass)
20	-6.3	$-8.7 \sim -3.7$	合格(Pass)
31.5	-3.1	$-5.0 \sim -1.0$	合格(Pass)
63	-0.9	$-2.3 \sim +0.7$	合格(Pass)
125	-0.2	$-1.7 \sim +1.3$	合格(Pass)
250	0.0	$-1.4 \sim +1.4$	合格(Pass)
500	0.0	$-1.4 \sim +1.4$	合格(Pass)
1000(ref.)	0.0	$-1.1 \sim +1.1$	合格(Pass)
2000	-0.2	$-1.8 \sim +1.4$	合格(Pass)
4000	-1.0	$-2.4 \sim +0.8$	合格(Pass)
8000	-3.2	$-6.1 \sim -0.9$	合格(Pass)
16000	-8.3	$-25.5 \sim -5.0$	合格(Pass)
20000	-10.7	$-\infty \sim -7.2$	合格(Pass)

表3 Table 3

标称频率 (Hz)	实测值Z计权 (dB)	允许范围 (dB)	结论
Nominal frequency	Measured Value Z-weighting	Tolerance	Conclusion
10	-1.4	$-\infty \sim +3.5$	合格(Pass)
20	-0.4	$-2.5 \sim +2.5$	合格(Pass)
31.5	-0.2	$-1.5 \sim +1.5$	合格(Pass)
63	-0.1	$-1.5 \sim +1.5$	合格(Pass)
125	0.0	$-1.5 \sim +1.5$	合格(Pass)
250	0.0	$-1.4 \sim +1.4$	合格(Pass)
500	0.0	$-1.4 \sim +1.4$	合格(Pass)
1000(ref.)	0.0	$-1.1 \sim +1.1$	合格(Pass)
2000	0.0	$-1.6 \sim +1.6$	合格(Pass)
4000	0.0	$-1.6 \sim +1.6$	合格(Pass)
8000	0.0	$-3.1 \sim +2.1$	合格(Pass)
16000	+0.1	$-17.0 \sim +3.5$	合格(Pass)
20000	0.0	$-\infty \sim +4.0$	合格(Pass)



校准结果

RESULTS OF CALIBRATION

证书编号: SSD201406950
Certification No.

原始记录编号: 2201406950
Record No.

第 5 页, 共 6 页
Page of

4 级线性 (参考频率 1 kHz)

Level linearity error (Reference frequency 1 kHz)

4.1 级程变化误差 (参考频率: 1000 Hz): 见表4

Level Change Error(Reference frequency: 1000 Hz): Showed in table 4

表4 Table 4

标准值 (dB)	指示值 (dB)	误差 (dB)	允差 (dB)	结论
Reference Value	Indication Value	Error	Tolerance	Conclusion
20	19.4	-0.6	±0.7	合格(Pass)
30	30.2	+0.2	±0.7	合格(Pass)
40	40.4	+0.4	±0.7	合格(Pass)
50	50.2	+0.2	±0.7	合格(Pass)
60	60.1	+0.1	±0.7	合格(Pass)
70	70.1	+0.1	±0.7	合格(Pass)
80	80.1	+0.1	±0.7	合格(Pass)
90(ref.)	90.0	0.0	----	合格(Pass)
100	100.1	+0.1	±0.7	合格(Pass)
110	110.1	+0.1	±0.7	合格(Pass)
120	120.1	+0.1	±0.7	合格(Pass)
130	130.0	0.0	±0.7	合格(Pass)

4.2 参考级量程

Reference range

起始点指示声级: 90 dB

Start point

起始点以上间隔 1 dB点的最大误差: 0.1 dB

Maximum Error for each 1 dB above start point

起始点以下间隔 1 dB点的最大误差: 0.1 dB

Maximum Error for each 1 dB below start point



校准结果 RESULTS OF CALIBRATION

证书编号: SSD201406950
Certification No.

原始记录编号: 2201406950
Record No.

第 6 页, 共 6 页
Page of

5 本机噪声:

Residual noise

A计权: <20 dB 结论: 合格(Pass)

A-weighting Conclusion

6 F和S时间计权:

Time weightings F/S

衰减速率: $F: >25 \text{ dB/s}$ (允许范围: $\geq 25 \text{ dB/s}$);

Attenuation rate Tolerance

$S: 4.5 \text{ dB/s}$ (允许范围: $3.4 \text{ dB/s} \sim 5.3 \text{ dB/s}$);

Tolerance

F和S差值: 0.0 dB

Dispersion F/S

7 过载指示:

Over loading indication

误差: 1.3 dB (允许范围: $\leq 1.8 \text{ dB}$) 结论: 合格(Pass)

Error Tolerance Conclusion

说明(Note):

1 声压级测量结果扩展不确定度:

Expanded uncertainty of measurement in Sound Pressure Level Calibration:

10 Hz~200 Hz, $U=0.5 \text{ dB}$, $k=2$

250 Hz~400 Hz, $U=0.4 \text{ dB}$, $k=2$

500 Hz~1.25 kHz, $U=0.4 \text{ dB}$, $k=2$

1.6 kHz~10 kHz, $U=0.6 \text{ dB}$, $k=2$

12.5 kHz~20 kHz, $U=1.0 \text{ dB}$, $k=2$

(依据JJF 1059.1-2012 测量不确定度评定与表示)

(According to JJF 1059.1-2012 Evaluation and Expression of Uncertainty in Measurement)

2 参考IEC 61672-1-2002标准。

Reference standard: IEC 61672-1-2002.

3 建议校准周期不超过1年。

The period of calibration advised within one year.



华南国家计量测试中心
广东省计量科学研究院

SOUTH CHINA NATIONAL CENTER OF METROLOGY
GUANGDONG INSTITUTE OF METROLOGY



校准证书

CALIBRATION CERTIFICATE

证书编号 SSD201406951
Certificate No.

第 1 页, 共 4 页
Page of

委托方 Paul Y Construction Co. Ltd
Client

委托方地址
Add. of Client

计量器具名称 Sound Level Calibrator
Description

型号规格 105
Model/Type

制造厂 Pulsar
Manufacturer

出厂编号 60220
Serial No.

设备编号
Equipment No.

接收日期 2014 年 12 月 15 日
Date of Receipt Y M D

结论 符合JJG 176-2005中1级技术要求
Conclusion

校准日期 2014 年 12 月 17 日
Date of Calibration Y M D

批准人
Approved Signatory

核 验
Inspected by

校 准
Calibrated by

证书专用章
Stamp



本中心地址: 中国广州市广园中路松柏东街30号 邮政编码: 510405
电话: (8620)86594172 传真: (8620)86590743 投诉电话: (8620)26296063 E-mail: scm@scm.com.cn
Add: No.30, Songbaidong Street, Guangyuanzhong Road, Guangzhou, P. R. China
Post Code: 510405 Tel: (8620)86594172 Fax: (8620)86590743 Complaint Tel: (8620)26296063
证书真伪查询: www.scm.com.cn; www.mtsp.com Certificate AuthenticityIdentify: www.scm.com.cn; www.mtsp.com



说 明

证书编号 SSD201406951
Certificate No.

DIRECTIONS

第 2 页, 共 4 页
Page of

1. 本中心是国家质量监督检验检疫总局在华南地区设立的国家法定计量检定机构, 计量授权证书号是: (国) 法计 (2012) 01043号、(国) 法计 (2012) 01032号。本中心质量管理体系符合 ISO/IEC 17025:2005 标准的要求。

This laboratory is the National Legal Metrological Verification Institution in southern China set up by the General Administration of Quality Supervision, Inspection and Quarantine of the People's Republic of China (AQSIQ) under authorization certificates No.(2012)01043 & (2012)01032. The quality system is in accordance with ISO/IEC 17025:2005.

2. 本中心所出具的数据均可溯源至国家计量基准和国际单位制(SI)。

All data issued by this laboratory are traceable to national primary standards and International System of Units (SI).

3. 本次校准的技术依据:

Reference documents for the calibration:

JJG 176-2005 声校准器检定规程 V. R. of Sound Calibrators

4. 本次校准所使用的主要计量标准器具:

Major standards of measurement used in the calibration:

设备名称/型号 Name of Equipment /Model	编号 Serial No.	证书号/有效期 Certificate No. /Due Date	计量特性 Metrological Characteristic
PULSE分析系统 Pulse analyzer System /3560C (3110模块)	2392397	SSD201402188 /2015-04-24	电平: $U_{rel}=0.1\%$, 频率: $U_{rel}=0.001\%$ ($k=2$) Voltage: $U_{rel}=0.1\%$, Frequency: $U_{rel}=0.001\%$ ($k=2$)
声校准器 Sound Calibrator /4231	2713562	SSD201402647 /2015-05-26	1 级 Grade 1

5. 校准地点、环境条件:

Place and environmental conditions of the calibration:

地点 声学/振动实验室 温度 $(23 \pm 3) ^\circ\text{C}$ 相对湿度 $(30 \sim 40) \%$
Place Acoustics/Vibration Lab. Temperature R.H.

6. 被校准仪器限制使用条件:

Limiting condition of the instrument calibrated:

注: 1. 本证书校准结果只与受校准仪器有关。
2. 未经本机构书面批准, 不得部分复制此证书。

Note: 1. The results relate only to the items calibrated.

2. This certificate shall not be reproduced except in full, without the written approval of our laboratory.



校准结果

RESULTS OF CALIBRATION

证书编号: SSD201406951
Certification No.

原始记录编号: 2201406951
Record No.

第 3 页, 共 4 页
Page of

1 外观: 合格

Apparent inspection: Pass

2 声压级 (dB): 见表1

Sound Pressure Level: Showed in table 1

表1 Table 1

标称值 (dB) Nominal Value	实测值 (dB) Measured Value	允差 (dB) Tolerance	结论 Conclusion	稳定度 (dB) Stabilization	稳定度允差 (dB) Stabilization Tolerance	结论 Conclusion
94	93.81	±0.40	合格(Pass)	0.01	≤0.10	合格(Pass)

3 频率: 见表2

Frequency: Showed in table 2

表2 Table 2

标称值 (Hz) Nominal Value	实测值 (Hz) Measured Value	允差 (%) Tolerance	结论 Conclusion
1000	1000.30	±1.0	合格(Pass)

4 总失真: 见表3

Total harmonic distortion: Showed in table 3

表3 Table 3

频率 (Hz) Frequency	声压级 (dB) Sound Pressure Level	总失真 (%) Total Harmonic Distortion	允差 (%) Tolerance	结论 Conclusion
1000	94	0.1	≤3	合格(Pass)



校准结果

RESULTS OF CALIBRATION

证书编号: SSD201406951
Certification No.

原始记录编号: 2201406951
Record No.

第 4 页, 共 4 页
Page of

说明(Note):

1 测量结果扩展不确定度:

Expanded uncertainty of measurement:

声压级: $U=0.15$ dB, $k=2$

Sound Pressure Level Calibration

频率: $U_{rel}=0.1\%$, $k=2$

Frequency

失真度: $U_{rel}=1.4\%$, $k=2$

Harmonic distortion

(依据JJF 1059.1-2012测量不确定度评定与表示)

(According to JJF 1059.1-2012 Evaluation and Expression of Uncertainty in Measurement)

2 建议校准周期不超过1年。

The period of calibration advised within one year.

**APPENDIX D
UPDATED ENVIRONMENTAL
MITIGATION IMPLEMENTATION
SCHEDULE**

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
<i>Ecology (Construction Phase)</i>			
S7.6.2	-	<p><u>Tree Felling and Vegetation Clearance</u></p> <p>Tree felling and compensatory planting will be implemented in accordance with the requirements of ETWB TCW No. 3/2006 as far as practicable.</p> <p><u>Water Quality</u></p> <p>Good construction site practices as required in ProPECC PN1/94 will be followed as appropriate. Implementation of some good construction practices are presented as follows:</p> <ul style="list-style-type: none"> • Containment of silt runoff within the site boundary; • Appropriate storage and disposal of chemicals and chemical waste and the provision of sanitary facilities for on-site workers; • Erection of temporary geo-textile silt or sediment fences/oil traps around any earth-moving works to trap any sediments and prevent them from entering watercourses; • Avoidance of soil storage against trees or close to water bodies; • No on-site burning of waste; and; • Waste and refuse in appropriate receptacles. 	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>
<i>Landscape & Visual (Construction Phase)</i>			
S9.11	-	<p>The following good site practices and measures have been recommended:</p> <ul style="list-style-type: none"> • Re-use of Existing topsoil and fill generated from site • For soil conservation, existing topsoil shall be re-used where possible for new planting areas within the project. The construction program shall consider using the soil removed from one phase for backfilling another. Suitable storage ground, gathering ground and mixing ground may be set up on-site as necessary. • To maximise protection to existing trees, ground vegetation and the associated under storey habitats, construction contracts may designate “No-intrusion Zone” to various areas within the site boundary with rigid and durable fencing for each individual no-intrusion zone. The contractor should closely monitor and restrict the site working staff from entering the “no-intrusion zone”, even for indirect construction activities and storage of equipment. • All retained trees should be recorded photographically at the commencement of the Contract, and carefully protected during the construction period. Detailed tree protection specification shall be allowed for and included in the Contract Specification, which specifies the tree protection requirement, submission and approval system, and the tree monitoring system, 	<p>^</p> <p>^</p> <p>^</p> <p>^</p>

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> In addition, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works sites. 	^
Table 9.7	CM1	<u>Site Hoarding</u> Erection of solid screen during construction stage to prevent undesirable views of the construction site from visually sensitive areas.	^
Table 9.7	CM2	<u>Management of facilities on work sites</u> To provide proper site management of the facilities on the sites, give control on the height and disposition/ arrangement of all welfare facilities and construction plant on site to minimise landscape and visual impacts to adjacent VSRs and existing/retained site features.	^
Table 9.7	CM3	<u>Construction programme</u> Employ construction techniques which assist in streamlining construction programme, minimise the duration of plant operations. Consider prefabrication of building elements offsite to minimise on site works and construction period.	^
<i>Air Quality</i>			
-	-	<u>Emission from Vehicles and Plants</u> <ul style="list-style-type: none"> All vehicles shall be shut down in intermittent use. Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke. All diesel fuelled construction plant within the works areas shall be powered by ultra-low sulphur diesel fuel (ULSD) 	^ * ^
<i>Construction Dust Impact</i>			
S6.3.3	-	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation potential dust impacts. 8-time watering per day on exposed worksites is recommended during construction phase to further alleviate the potential construction dust impacts.	^
S6.3.3	-	<ul style="list-style-type: none"> Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones. The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from 	^ ^ ^ ^

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		<p>the vehicle;</p> <ul style="list-style-type: none"> • Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcore; • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing; Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; • The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Any skip hoist for material transport should be totally enclosed by impervious sheeting; • Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies. 	<p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">N/A⁽²⁾</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p>
Construction Airborne Noise			
S5.5.6	-	<p>Implement the following good site practices:</p> <ul style="list-style-type: none"> • Louvres should be orientated away from adjacent NSRs, preferably onto the main line of WRL which are less sensitive. • Direct noise mitigation measures including silencers, acoustic louvers and acoustic enclosures should be allowed for in the design for the maintenance buildings, plant buildings and workshops. • The façade and doors for these plant / workshops would have adequate sound insulation properties to minimise the noise emanating through the building fabric to acceptable level. 	<p style="text-align: center;">N/A⁽²⁾</p> <p style="text-align: center;">N/A⁽²⁾</p> <p style="text-align: center;">^</p>

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> Acoustic treatments such as silencer, acoustic louvers, noise barriers and acoustic enclosures should be installed for the existing equipment where necessary to minimise the cumulative noise impacts on the NSRs. 	^
Water Quality (Construction Phase)			
S12.5	-	<p>In accordance with the Practice Noise for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following:</p> <p><u>Construction Runoff and Site Drainage</u></p> <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction. The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1m³/s a sedimentation basin of 30m³ would be required and for a flow rate of 0.5 m³/s the basin would be 150 m³. The detailed design of the sand/silt traps shall be undertaken by the Contractor prior to the commencement of construction. All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means. The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows. All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and 	<p style="text-align: center;">#</p> <p style="text-align: center;">^</p> <p style="text-align: center;">N/A⁽²⁾</p> <p style="text-align: center;">^</p> <p style="text-align: center;">N/A⁽²⁾</p> <p style="text-align: center;">#</p>

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		<p>particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.</p> <ul style="list-style-type: none"> • Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. • Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. • Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. • Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. • All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. • Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain. 	<p>N/A⁽²⁾</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p>N/A⁽²⁾</p> <p style="text-align: center;">^</p> <p>N/A⁽²⁾</p>
S12.5.1.2	-	<p><u>Sewage Effluent</u></p> <ul style="list-style-type: none"> • Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance. 	<p style="text-align: center;">^</p>
S12.5.1.3	-	<p><u>Accidental Spillage</u></p> <ul style="list-style-type: none"> • In order to prevent accidental spillage of chemicals, proper storage and handling facilities should be provided. All the tanks, containers, storage area should be banded 	<p style="text-align: center;">*</p>

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		and the locations should be locked as far as possible from the sensitive watercourse and storm water drains. The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings. Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste disposal (Chemical Waste) (General) Regulation.	
Waste Management (Construction Waste)			
S11.5.1	-	A trip-ticket system should be established and will comply with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation to monitor the disposal of public fill and solid wastes at public filling facilities and landfills, and to control fly-tipping.	^
S11.5.1	-	<p><u>C & D Material</u></p> <ul style="list-style-type: none"> • Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; • Carry out on-site sorting; • Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; • Adopt “Selective Demolition” technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; • Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; and • Implement an enhanced Waste Management Plan, which become a part of the Environmental Management Plan in accordance with “ETWBTC (Works) No. 19/2005 – Waste Management on Construction Site”, to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction. • In addition, disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation. 	<p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">N/A⁽²⁾</p> <p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">^</p>
S11.5.1	-	<p><u>C&D Waste</u></p> <ul style="list-style-type: none"> • Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. • The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or 	<p style="margin-left: 100px;">^</p> <p style="margin-left: 100px;">*</p>

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.	
S11.5.1	-	<p><u>General Refuse</u></p> <ul style="list-style-type: none"> • General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. • Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible. • Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. In addition, waste separation facilities for paper, aluminium cans, plastic bottles etc., should be provided. 	* ^ ^
S11.5.1	-	<p><u>Chemical Waste</u></p> <p>Chemical waste producers should be registered with EPD. For those processes which generate chemical waste, the Contractor shall identify any alternatives that generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste.</p> <p>Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows.</p> <p>Containers used for storage of chemical wastes should:</p> <ul style="list-style-type: none"> • Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; • Have a capacity of less than 450 L unless the specification have been approved by EPD; and • Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations. <p>The storage area for chemical wastes should:</p> <ul style="list-style-type: none"> • Be clearly labelled and used solely for the storage of chemical wastes; • Be enclosed on at least 3 sides; • Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; 	^ N/A ⁽²⁾ ^ ^ ^

Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR ⁽¹⁾ Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> • Have adequate ventilation; • Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste, if necessary); and • Be arranged so that incompatible materials are adequately separated. <p>Disposal of chemical waste should:</p> <ul style="list-style-type: none"> • Be via a licensed waste collector; and • Be to a facility licensed to receive chemical waste, such as the CWTC which also offers a chemical waste collection service and can supply the necessary storage containers; or • Be to a re-user of the waste, under approval from EPD. 	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>N/A⁽²⁾</p>

Remarks:

(1) The latest Environmental Review Report (ERR) for Pat Heung Depot Modification Works is referred in preparation of this summary.

^ Compliance of mitigation measure X Non-compliance of mitigation measure

- Non-compliance but rectified by the contractor

- * Recommendation was made during site audit but improved/rectified by the contractor.

- # Recommendation was made during site audit but not yet improved/rectified by the contractor.

N/A⁽¹⁾ Not Applicable

N/A⁽²⁾ Not Applicable at this stage

**APPENDIX E
ENVIRONMENTAL MONITORING
SCHEDULE**

Contract No. SCL 1117
 Pat Heung Depot Modification Works
 Impact Noise Monitoring Schedule for Feb 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Feb	2-Feb	3-Feb	4-Feb	5-Feb	6-Feb	7-Feb
	Noise (1) at NM1, NM2 & NM3A					
8-Feb	9-Feb	10-Feb	11-Feb	12-Feb	13-Feb	14-Feb
				Noise (1) at NM1, NM2 & NM3A		
15-Feb	16-Feb	17-Feb	18-Feb	19-Feb	20-Feb	21-Feb
		Noise (1) at NM1, NM2 & NM3A				
22-Feb	23-Feb	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb
				Noise (1) at NM1, NM2 & NM3A		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Noise Monitoring Station:

NM1 - Tourmaline Villa
 NM2 - Kam Po Road
 NM3A - Tai Kek Tsuen

Category	Time Period
(1)	0700-1900 hrs on normal weekdays

Contract No. SCL 1117
 Pat Heung Depot Modification Works
 Tentative Impact Noise Monitoring Schedule for Mar 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Mar	2-Mar	3-Mar	4-Mar	5-Mar	6-Mar	7-Mar
				Noise (1) at NM1, NM2 & NM3A		
8-Mar	9-Mar	10-Mar	11-Mar	12-Mar	13-Mar	14-Mar
				Noise (1) at NM1, NM2 & NM3A		
15-Mar	16-Mar	17-Mar	18-Mar	19-Mar	20-Mar	21-Mar
				Noise (1) at NM1, NM2 & NM3A		
22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar
				Noise (1) at NM1, NM2 & NM3A		
29-Mar	30-Mar	31-Mar				

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Noise Monitoring Station:

NM1 - Tourmaline Villa
 NM2 - Kam Po Road
 NM3A - Tai Kek Tsuen

Category	Time Period
(1)	0700-1900 hrs on normal weekdays

**APPENDIX F
NOISE MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**




Appendix F - Noise Monitoring Results

Location NM1 - Tourmaline Villa							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Feb-15	9:28	Sunny	68.6	73.1	51.1	61.2	67.7
12-Feb-15	9:36	Sunny	58.4	59.5	48.8		58.4 Measured \leq Baseline
17-Feb-15	9:49	Cloudy	64.6	64	46.2		61.9
26-Feb-15	10:28	Sunny	59	58.7	47.3		59 Measured \leq Baseline

Location NM2 - Kam Po Road							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Feb-15	10:08	Sunny	58.3	60.2	50.1	61.3	58.3 Measured \leq Baseline
12-Feb-15	10:15	Sunny	62.4	63.4	50.2		55.9
17-Feb-15	10:31	Cloudy	60.5	60.6	46.6		60.5 Measured \leq Baseline
26-Feb-15	11:07	Sunny	59.5	60.7	49.1		59.5 Measured \leq Baseline

Location NM3A - Tai Kek Tsuen							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Feb-15	8:44	Sunny	67.7	66.8	55.2	66.7	60.8
12-Feb-15	8:36	Sunny	68.1	64.2	52.4		62.5
17-Feb-15	9:08	Cloudy	62.1	64	53.5		62.1 Measured \leq Baseline
26-Feb-15	9:44	Sunny	71.2	61.3	52.1		69.3

Noise Levels

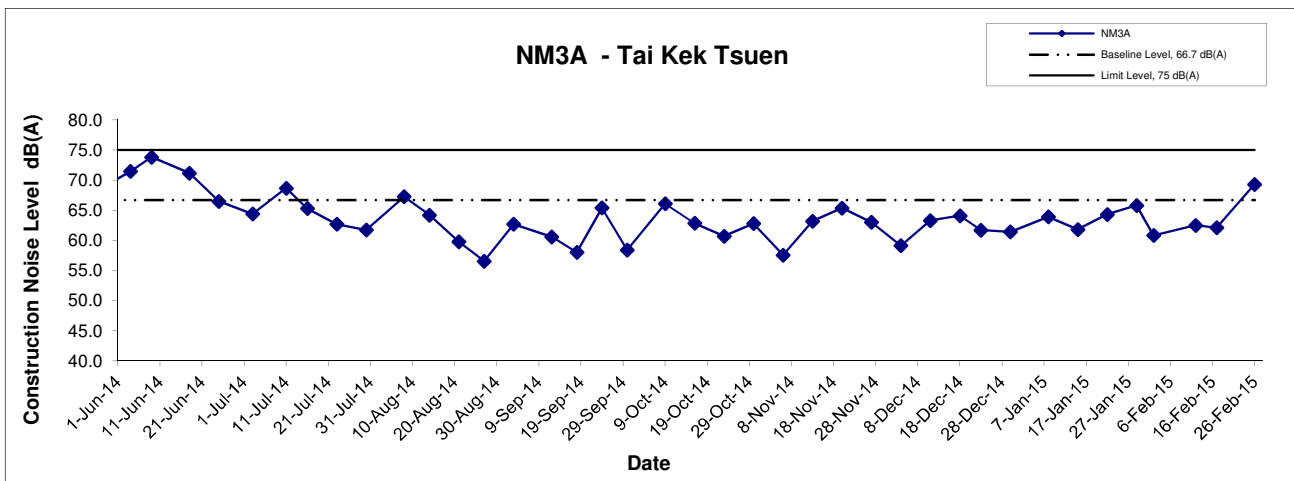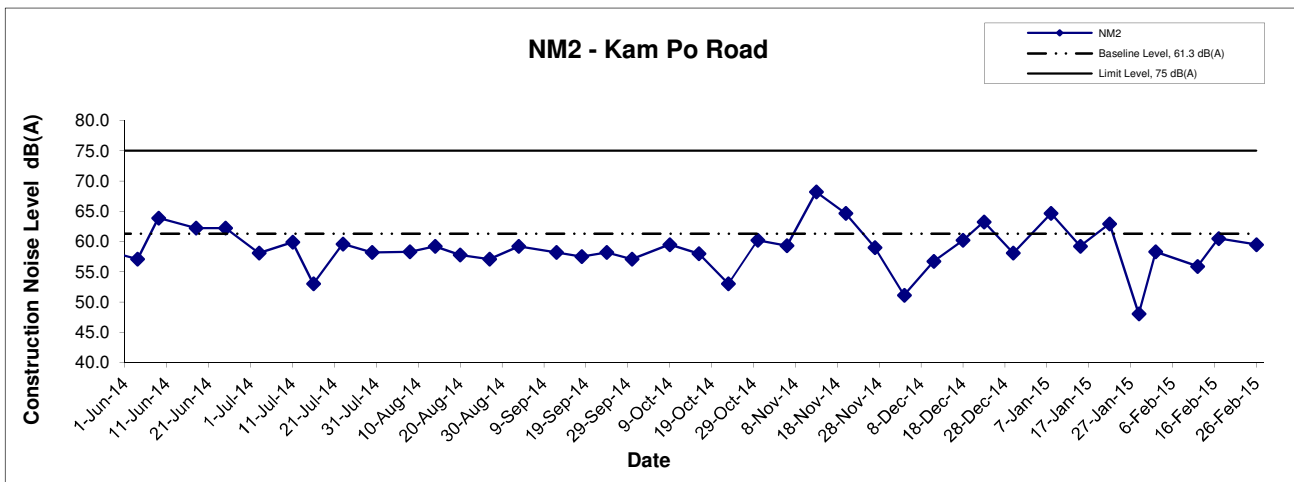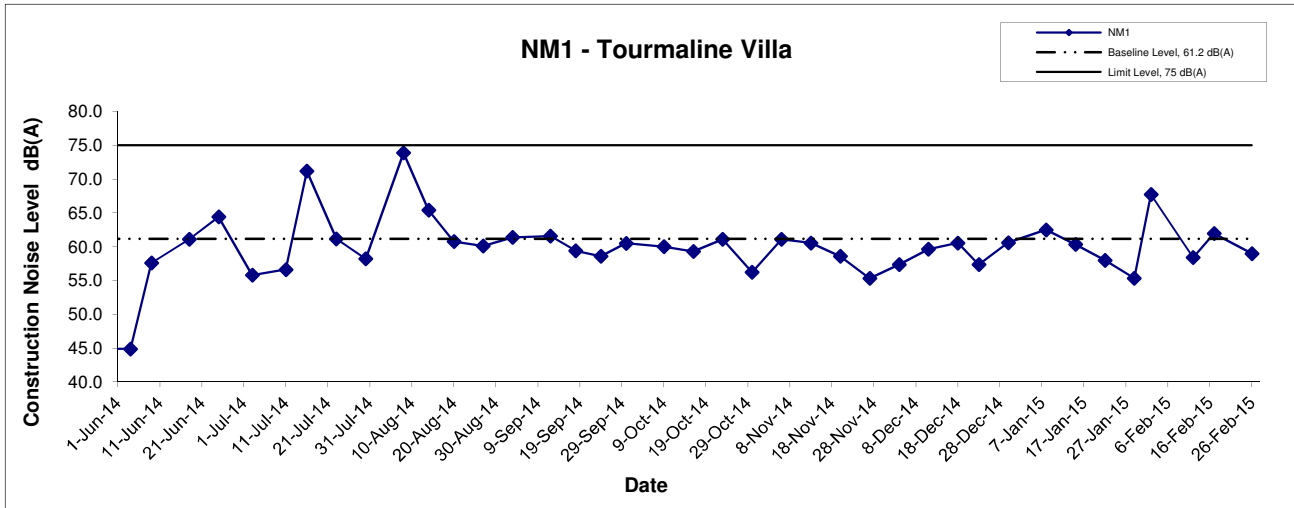

Title MTR Works Contract 1117 Pat Heung Depot Modification Works Graphical Presentation of the Construction Noise Monitoring Results	Scale N.T.S	Project No. MA13003	
	Date Feb-15	Appendix F	

**APPENDIX G
WASTE GENERATION IN THE
REPORTING MONTH**

Paul Y. Construction Company, Limited
MTR Contract 1117
Pat Heung Depot Modification Works

Monthly Summary Waste Flow Table for 2015 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed to Sorting Facilities	Disposed to Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in kg)	(in kg)	(in kg)	(in '000m ³)
Jan '15	2.781	-		-	0.114	2.667	-	65.15	175	-	-	0.006
Feb '15	1.690	-	-	-	0.074	1.617	-	-	315	-	-	0.058
Mar '15	-	-	-	-	-	-	-	-	-	-	-	-
Apr '15	-	-	-	-	-	-	-	-	-	-	-	-
May '15	-	-	-	-	-	-	-	-	-	-	-	-
Jun '15	-	-	-	-	-	-	-	-	-	-	-	-
Sub-total	-	-	-	-	-	-	-	-	-	-	-	-
Jul '15	-	-	-	-	-	-	-	-	-	-	-	-
Aug '15	-	-	-	-	-	-	-	-	-	-	-	-
Sep '15	-	-	-	-	-	-	-	-	-	-	-	-
Oct '15	-	-	-	-	-	-	-	-	-	-	-	-
Nov '15	-	-	-	-	-	-	-	-	-	-	-	-
Dec '15	-	-	-	-	-	-	-	-	-	-	-	-
Total												

Note:

Assume the densities of Rock, Soil, Mix Rock and Soil are Regular Spoil to be 2.0 tonnes/m³. Assumption the densities of general refuse is 1.0 tonnes/m³

APPENDIX H
SITE AUDIT SUMMARY

Shatin to Central Link -

Contract 1117 Pat Heung Depot Modification Works



Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	150203
Date	3 February 2015 (Tuesday)
Time	09:00 -12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
150203-O01	<p>Part B - Water Quality</p> <ul style="list-style-type: none"> Sediment and general refuse in the sedimentation tank should be cleared to maintain the discharge water quality (Area A); Muddy water is observed in the drainage channels, access to the channels should be blocked to prevent road wash water from entering (Area C, A 100, near Area D) <p>Part C - Tree Management Protection / Landscape & Visual Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part D - Air Quality</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part E - Construction Noise Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. 	B 1 & B 6iii
150203-O02 150203-R03	<p>Part F - Waste/Chemical Management</p> <ul style="list-style-type: none"> Containers should be provided with drip tray (Area A). The u-channel near S-18 should be maintained by clearing any accumulated oil stain (Area A). <p>Part G - Permit / Licenses</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part H - Remark</p> <ul style="list-style-type: none"> Follow-up on previous audit sessions (ref: 150127): outstanding item of 150127-O01 and 150127-O02 will be followed up during the next site inspection. 	F 9 F 6

	Name	Signature	Date
Recorded by	Victor Wong		3 February 2015
Checked by	Dr. Priscilla Choy		3 February 2015

**Shatin to Central Link -
Contract 1117 Pat Heung Depot Modification Works**



Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	150211
Date	11 February 2015 (Wednesday)
Time	09:30 -12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
150211-001	<p>Part B - Water Quality</p> <ul style="list-style-type: none"> Oil observed in the u-channel should be cleared; The sand bags in the u-channel should be replaced and provided with oil absorbent materials (Area A, near Option 1). <p>Part C - Tree Management Protection / Landscape & Visual Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part D - Air Quality</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part E - Construction Noise Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part F - Waste/Chemical Management</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part G - Permit / Licenses</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part H - Remark</p> <ul style="list-style-type: none"> - 	B 8 & B 9i

	Name	Signature	Date
Recorded by	Victor Wong		11 February 2015
Checked by	Dr. Priscilla Choy		11 February 2015

*Shatin to Central Link -
Contract 1117 Pat Heung Depot Modification Works*



Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	150216
Date	16 February 2015 (Monday)
Time	14:00 -17:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
150216-O01	<p>Part B - Water Quality</p> <ul style="list-style-type: none"> Cloudy water is observed in the sedimentation tank (Area A); discharge water quality in Area A should be improved by adjusting the chemical dosage of the tank. 	B 6iii & B 8
150216-R02	<p>Part C - Tree Management Protection / Landscape & Visual Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part D - Air Quality</p> <ul style="list-style-type: none"> Black smoke emission is observed from the excavator in Area B. <p>Part E - Construction Noise Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. 	D 17
150216-R03	<p>Part F - Waste/Chemical Management</p> <ul style="list-style-type: none"> General refuse and other waste should be stored in designated containers and removed regularly (Area C and D). <p>Part G - Permit / Licenses</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part H - Remark</p> <ul style="list-style-type: none"> Follow-up on previous audit sessions (ref: 150211); all environmental deficiencies were improved by the Contractor. 	F 1i & F 1iii

	Name	Signature	Date
Recorded by	Victor Wong		16 February 2015
Checked by	Dr. Priscilla Choy		16 February 2015

**Shatin to Central Link -
Contract 1117 Pat Heung Depot Modification Works**



Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	150224
Date	24 February 2015 (Tuesday)
Time	09:00 -11:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
150224-R02	<p>Part B - Water Quality</p> <ul style="list-style-type: none"> The Contractor is reminded to clear the accumulated mud and other waste in the u-channel regularly (Area C, A100). 	B 8
150224-R01	<p>Part C - Tree Management Protection / Landscape & Visual Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part D - Air Quality</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part E - Construction Noise Impact</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part F - Waste/Chemical Management</p> <ul style="list-style-type: none"> Construction equipment and materials should be stored properly in the identified area (Area B). <p>Part G - Permit / Licenses</p> <ul style="list-style-type: none"> No environmental deficiency was identified during the site inspection. <p>Part H - Remark</p> <ul style="list-style-type: none"> - 	F 7

	Name	Signature	Date
Recorded by	Victor Wong		24 February 2015
Checked by	Dr. Priscilla Choy		24 February 2015

**APPENDIX I
SUMMARY OF EXCEEDANCE**

APPENDIX I – SUMMARY OF EXCEEDANCE

Reporting Month: February 2015

a) Exceedance Report for Noise Monitoring (NIL)

**APPENDIX J
CUMULATIVE LOG FOR COMPLAINTS,
NOTIFICATIONS OF SUMMONS AND
SUCCESSFUL PROSECUTIONS**

Appendix J - Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions

Cumulative Complaint Log

Log Ref.	Date/Location	Complainant/ Date of Contact	Details of Complaint	Investigation/ Mitigation Action	File Closed
--	--	--	--	--	--

Cumulative Log for Notifications of Summons

Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since project commencement
--	--	--	--	--	--

Cumulative Log for Successful Prosecutions

Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since the commencement of the project
--	--	--	--	--	--
