

Our ref.: CCL/MA13003/Corres/Out/bw160414\_Mrpt1603

Environmental Protection Department  
Environmental Assessment Division  
Assessment and Noise Group  
27<sup>th</sup> Floor, Southorn Centre,  
130 Hennessy Road  
Wan Chai, Hong Kong

By Courier

14 April 2016

Attn.: Mr. LAM Wah King, Edward

Dear Sirs,

**Environmental Permit (EP) No. FEP-24/004/1998/I**  
**West Rail, Phase I - MTRC Works Contract 1117**  
**Pat Heung Depot Modification Works**


**- Monthly Noise Monitoring Report (March 2016) for Pat Heung Depot Modification Works**

On behalf of MTRCL, we are pleased to submit herewith three hard copies and one electronic copy of the captioned report in accordance with Condition 4.5 of the Project EP.

Please kindly note that the captioned report has been certified by the Environmental Team (ET) Leader and verified by the Independent Environmental Checker (IEC) as per Condition 4.5 of the Project EP.

Should you require any further information, please feel free to contact our Mr. Benjamin Wong at 2151-2098 or the undersigned at 2151 2089.

Yours faithfully,  
Cinotech Consultants Ltd.

  
Dr. Priscilla Choy  
Environmental Team Leader

Encl.

Cc. (all w/e)


EPD	(Attn: Mr. Wai CHAU)	w/encl.
MTRCL	(Attn: Mr. Richard KWAN)	w/o encl.
Paul Y	(Attn: Mr. Edmond Chan)	w/encl.

**Paul Y. Construction Company, Limited**

**MTR Works Contract 1117-  
Pat Heung Depot Modification Works**

**Monthly Noise Monitoring Report  
for  
March 2016**

(Version 1.0)

Certified By	 Environmental Team Leader (Dr. Priscilla Choy)
--------------	---

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

**CINOTECH CONSULTANTS LTD**

Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Tel: (852) 2151 2083 Fax: (852) 3107 1388


Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)

MTR Corporation Limited

## West Rail

Pat Heung Modification Works  
Monthly Noise Monitoring Report No. 37  
[Period from 1 to 31 March 2016]

(April 2016)

Verified by:                     Fredrick Leong                     

Position: Independent Environmental Checker

Date:                     14 Apr. 2016

## TABLE OF CONTENTS

	Page
<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
Introduction .....	1
Summary of Construction Works undertaken during Reporting Period .....	1
Environmental Monitoring and Audit Progress .....	1
Noise.....	1
Waste Management .....	1
Environmental Site Inspection .....	2
Environmental Exceedance/Non-conformance/Complaint/Summon and Prosecution.....	2
Future Key Issues .....	2
<b>1 INTRODUCTION .....</b>	<b>2</b>
Purpose of the Report .....	3
Structure of the Report .....	3
<b>2 PROJECT INFORMATION.....</b>	<b>4</b>
Background .....	4
General Site Description .....	4
Construction Programme and Activities .....	4
Project Organisation .....	4
Status of Environmental Licences, Notification and Permits.....	5
Summary of EM&A Requirements .....	6
<b>3 ENVIRONMENTAL MONITORING REQUIREMENTS.....</b>	<b>7</b>
Construction Noise Monitoring.....	7
Monitoring Requirements.....	7
Monitoring Equipment .....	8
Monitoring Parameters, Frequency and Duration .....	8
Monitoring Methodology and QA/QC Procedures .....	8
<b>4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS .....</b>	<b>9</b>
<b>5 MONITORING RESULTS .....</b>	<b>10</b>
Noise.....	10
Waste Management .....	10
<b>6 ENVIRONMENTAL SITE INSPECTION.....</b>	<b>11</b>
Site Audits .....	11
Implementation Status of Environmental Mitigation Measures.....	11
<b>7 ENVIRONMENTAL NON-CONFORMANCE.....</b>	<b>14</b>
Summary of Exceedances .....	14
Summary of Environmental Non-Compliance.....	14
Summary of Environmental Complaint .....	14
Summary of Environmental Summon and Successful Prosecution .....	14
<b>8 FUTURE KEY ISSUES .....</b>	<b>15</b>
Key Issues in the Coming Month .....	15
Monitoring Schedule for the Next Month .....	15
Construction Programme for the Next Month.....	15

<b>9 CONCLUSIONS.....</b>	<b>15</b>
Conclusions .....	15
Recommendations .....	16

## LIST OF TABLES

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 2.1	Status of Environmental Licenses, Notification and Permits
Table 3.1	Construction Noise Monitoring Stations
Table 3.2	Criteria for Action and Limit Levels for Construction Noise
Table 3.3	Noise Monitoring Equipment
Table 3.4	Noise Monitoring Parameters, Frequency and Duration
Table 4.1	Status of Required Submissions under EP
Table 5.1	Quantities of Waste Generated from the Project
Table 6.1	Site Audit Observations

## LIST OF FIGURES

Figure 1	Site Layout Plan
Figure 2	Project Organization Chart for Environmental Works
Figure 3	Location of Construction Noise Monitoring Stations

## LIST OF APPENDICES

Appendix A	Tentative Construction Programme
Appendix B	Event and Action Plan
Appendix C	Copies of Calibration Certificates
Appendix D	Updated Environmental Mitigation Implementation Schedule
Appendix E	Environmental Monitoring Schedule
Appendix F	Noise Monitoring Results and Graphical Presentations
Appendix G	Waste Generation in the Reporting Month
Appendix H	Site Audit Summary
Appendix I	Summary of Exceedance
Appendix J	Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions

## EXECUTIVE SUMMARY

### Introduction

1. This is the 37<sup>th</sup> Monthly Noise Monitoring Report prepared by Cinotech Consultants Limited for MTR Works Contract 1117 - Pat Heung Depot (PHD) Modification Works. This report documents the findings of EM&A Works conducted from 1 March to 31 March 2016 since major construction works for Contract 1117 commenced on 1 March 2013.

### Summary of Construction Works undertaken during Reporting Period

2. The major site activities undertaken in the reporting period include:
  - Site clearance and formation, site surveying
  - Sheet-piling
  - Drainage works, manholes construction
  - ABWF Works
  - Cross track ducts construction
  - Cable trough laying
  - Strengthening works for OHL Mast at Location 2
  - Hydroseeding
  - Construction of FAO Fencing
3. As of this reporting period, there is no record of any project changes from that originally proposed as described in the latest Environmental Review Report (ERR) for this Works Contract 1117.

### Environmental Monitoring and Audit Progress

4. A summary of the monitoring activities in this reporting period is listed below:
  - Construction Noise Monitoring during normal weekdays
    - NM1 4 times
    - NM2 4 times
    - NM3A 4 times
    - Environmental Site Inspection 5 times

### Noise

5. 4 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations during normal weekdays of the reporting period. No exceedance was recorded during the reporting period.

### Waste Management

6. Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. About 606 m<sup>3</sup> of inert C&D materials were generated during the reporting period. Non-inert C&D wastes include 0 kg of metals, 221 kg of paper/cardboard packaging materials and 7 m<sup>3</sup> of general refuse were generated during the reporting period. The inert C&D materials generated from the

Project were disposed of at TM 38 Area Fill Bank, while all non-inert waste was disposed of at NENT.

### Environmental Site Inspection

7. A monthly joint environmental site inspection was carried out by the representatives of the Contractor, the IEC and the ET. Details of the audit findings and implementation status are presented in Section 6.

### Environmental Exceedance/Non-conformance/Complaint/Summon and Prosecution

8. Summary of the events and action taken and key information in the reporting month is tabulated in **Table I** and **Table II** respectively.

**Table I Summary Table for Events Recorded in the Reporting Month**

Parameter	No. of Exceedance		Action Taken
	Action Level	Limit Level	
Impact Noise Monitoring	0	0	N/A

**Table II Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Notifications of any summons & prosecutions	0	---	N/A	N/A	---

### Future Key Issues

9. Major site activities for the coming reporting month will include:
- Site clearance and formation, site surveying
  - Drainage works, manholes construction
  - ABWF Works
  - Cross track ducts construction
  - Cable trough laying
  - Strengthening works for OHL Mast at Location 2
  - Hydroseeding
  - Construction of FAO Fencing

## 1 INTRODUCTION

- 1.1 Cinotech Consultants Limited (Cinotech) is commissioned by Paul Y. Construction

Company, Limited as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme during construction phase of the MTR Works Contract 1117 –Pat Heung Depot (PHD) Modification Works (hereafter referred to “the Project”).

### **Purpose of the Report**

- 1.2 This is the 37<sup>th</sup> Monthly Noise Monitoring Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 March to 31 March 2016 since major construction works for Contract 1117 commenced on 1 March 2013.

### **Structure of the Report**

- 1.3 The structure of the report is as follows:

Section 1: **Introduction** - details the scope and structure of the report.

Section 2: **Project Information** - summarises background and scope of the project, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permits/Licenses during the reporting period.

Section 3: **Environmental Monitoring Requirement** - summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event / Action Plans, environmental mitigation measures as recommended in the Environmental Review Report (ERR) and relevant environmental requirements.

Section 4: **Implementation Status on Environmental Mitigation Measures** - summarises the implementation of environmental protection measures during the reporting period.

Section 5: **Monitoring Results** - summarises the monitoring results obtained in the reporting period.

Section 6: **Environmental Site Inspection** - summarises the audit findings of the weekly site inspections undertaken within the reporting period.

Section 7: **Environmental Non-conformance** - summarises any monitoring exceedance, environmental complaints and environmental summons within the reporting period.

Section 8: **Future Key Issues** - summarises the impact forecast and monitoring schedule for the next three months.

Section 9: **Conclusions and Recommendations**



## 2 PROJECT INFORMATION

### Background

- 2.1 West Rail Line (WRL) is one of the strategic rail infrastructures in Hong Kong providing the people of Hong Kong an environmentally friendly and convenient way to travel between the western part of the New Territories and western Kowloon. Under the approved WRL Environmental Impact Assessment (EIA) Report (EIA-149/BC), it has a total length of about 30.5km with 9 stations, including Nam Cheong, Mei Foo, Tsuen Wan West, Kam Sheung Road, Yuen Long, Long Ping, Tin Shui Wai, Siu Hong, Tuen Mun and one depot at Pat Heung.
- 2.2 The EIA Report of WRL was prepared and submitted to Environmental Protection Department (EPD) prior to the enactment of the Environmental Impact Assessment Ordinance (EIAO) in 1998. Since the first Environmental Permit (EP) (EP-004/1998), there have been amendments made to the permit through a number of EP variation applications related to the main line of WRL.
- 2.3 This Works Contract 1117 covers the modification works at the existing Pat Heung Depot (PHD) of WRL to meet future operational and maintenance requirements. The PHD modification works include the construction of a new train wash plant, locomotive shed, permanent - way workshop, stabling sidings, extension of maintenance building and modification of noise barriers.
- 2.4 Since the modification works at PHD forms part of the WRL, a variation of environmental permit (VEP) was applied and a VEP (EP No. EP-004/1998/I) were subsequently granted. Moreover, a further Environmental Permit (FEP) (EP No: FEP-24/004/1998/I) on construction and operation of WRL (including the PHD modification works) was issued by Director of Environmental Protection (DEP) to the MTR Corporation Limited on 23 July 2012.

### General Site Description

- 2.5 The site layout and proposed modification works are illustrated in **Figure 1**.

### Construction Programme and Activities

- 2.6 A summary of the major construction activities undertaken in this reporting period is shown as follows. The tentative construction programme is presented in **Appendix A**.
- Site clearance and formation, site surveying
  - Sheet-piling
  - Drainage works, manholes construction
  - ABWF Works
  - Cross track ducts construction
  - Cable trough laying
  - Strengthening works for OHL Mast at Location 2
  - Hydroseeding
  - Construction of FAO Fencing

## Project Organisation

- 2.7 Different parties with different levels of involvement in the project organization include:
- Engineer or Engineer’s Representative (ER)– MTR Corporation (MTRC)
  - Contractor’s Environmental Team (Contractor’s ET) – Cinotech Consultants Ltd. (Cinotech)
  - Independent Environmental Checker (IEC) – Meinhardt Infrastructure and Environment Limited (MIEL)
  - Contractor – Paul Y. Construction Company, Limited(Paul Y)
- 2.8 The responsibilities of respective parties are detailed in Section 2 of the approved EM&A Programme for PHD Modification Works.
- 2.9 The project organisation including key personnel contact names and telephone numbers is presented in **Figure 2**.

## Status of Environmental Licences, Notification and Permits

- 2.10 A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project is presented in **Table 2.1**.

**Table 2.1 Status of Environmental Licenses, Notification and Permits**

Permit / License No.	Valid Period		Status
	From	To	
<b>Environmental Permit (EP)</b>			
FEP-24/004/1998/J	21/10/2013	End of the Project	Valid
<b>Notification pursuant to Air Pollution Control (Construction Dust) Regulation</b>			
No.351534	31/10/2012	N/A	Valid
<b>Billing Account for Construction Waste Disposal</b>			
Account No. 7016256	2/11/2012	N/A	Valid
<b>Registration of Chemical Waste Producer</b>			
5218-531-P2991-02	4/12/2012	N/A	Valid
<b>Effluent Discharge License under Water Pollution Control Ordinance (WPCO)</b>			
WT00015378-2013	26/3/2013	31/3/2018	Valid
<b>Construction Noise Permit</b>			
GW-RN0889-15 <b>(Area D: Location 2 OHL Footing and Noise Barrier Modification near to Kam Sheung Road Station) – 2<sup>nd</sup> renewal</b>	2/1/2016	1/4/2016	Updated to GW-RN0211-16
GW-RN0211-16 <b>(Area D: Location 2 OHL Footing and Noise Barrier Modification near to Kam Sheung Road Station) – 3<sup>rd</sup> renewal</b>	2/4/2016	1/7/2016	Valid

### **Summary of EM&A Requirements**

- 2.11 The EM&A programme under Works Contract 1117 require construction noise monitoring as well as environmental site audits. The EM&A requirements are described in the following sections, including:
- all monitoring parameters;
  - environmental quality performance limits (Action and Limit levels);
  - Event-Action Plans;
  - Environmental mitigation measures, as recommended in the Environmental Review Report (ERR) for the VEP (EP No. FEP-24/004/1998/I); and
  - Environmental requirements in contract documents.
- 2.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.
- 2.13 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely construction noise as well as audit works for the Project in the reporting month.

### 3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### Construction Noise Monitoring

##### Monitoring Requirements

- 3.1 Noise monitoring was conducted in accordance with the approved EM&A Programme for PHD Modification Works.
- 3.2 With reference to the baseline monitoring report for the Project, **Table 3.1** and **Table 3.2** summarises the location of noise monitoring stations and shows the established Action and Limit Levels for construction noise monitoring works respectively. Location of the monitoring stations is shown on **Figure 3**.

**Table 3.1 Construction Noise Monitoring Stations**

ID in the approved EM&A Programme	ID in Baseline Noise Monitoring Report	Construction Noise Monitoring Station
NM1	NM1	Tourmaline Villa
NM2	NM2	Kam Po Road
NM3	NM3A <sup>(1)</sup>	Tai Kek Tsuen

Note:

- (1) Since permission of access could not be obtained, an alternative location at a village house just next to the original proposed monitoring location in the EM&A Programme was adopted for the baseline noise monitoring.

**Table 3.2 Criteria for Action and Limit Levels for Construction Noise**

Time Period <sup>(1)</sup>	Noise Monitoring Station	Action Level	Limit Level, dB (A)
0700-1900 hrs of normal weekdays	Tourmaline Villa (NM1)	When one documented valid complaint is received.	75.0
	Kam Po Road (NM2)		
	Tai Kek Tsuen (NM3A)		

Note:

- (1) If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority should be followed.

- 3.3 Should non-compliance of the criteria in **Table 3.2** occur, action in accordance with the Event and Action Plan in **Appendix B** should be carried out.

## Monitoring Equipment

3.4 **Table 3.3** summarizes the noise monitoring equipment model being used.

**Table 3.3 Noise Monitoring Equipment**

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	Svantek Model 955 (Serial no. 27455);	1
Calibrator	Pulsar Instruments Model 105 (Serial no. 51342)	1

## Monitoring Parameters, Frequency and Duration

3.5 **Table 3.4** summarizes the monitoring parameters, frequency and total duration of monitoring.

**Table 3.4 Noise Monitoring Parameters, Frequency and Duration**

Station	Parameter	Period	Frequency
NM1, NM2 and NM3A	$L_{eq,30 \text{ min.}}^{(1)}$ ( $L_{10}$ and $L_{90}$ were also recorded as supplementary information)	0700-1900 hours on normal weekdays	Once a week

Note (1):  $L_{eq, 30 \text{ min.}}$  as six consecutive  $L_{eq, 5 \text{ min}}$  readings.

## Monitoring Methodology and QA/QC Procedures

### Field Monitoring

3.6 The monitoring procedures are as follows:

- The microphone head of the sound level meter was positioned 1m exterior of the noise sensitive facade and lowered sufficiently so that the building's external wall acts as a reflecting surface.
- The battery condition was checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - Frequency weighting : A
  - Time weighting : Fast
  - Measurement time : 5 minutes (obtaining six consecutive  $L_{eq, 5 \text{ min}}$  readings for a  $L_{eq, 30 \text{ min.}}$  reading)
- Prior to and after noise measurement, the meter was calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
- The wind speed at the monitoring station was checked with the portable wind meter. Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

- Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- At the end of the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- A façade correction of +3dB (A) shall be made to the noise parameter obtained by free field measurement.

### *Maintenance and Calibration*

3.7 Maintenance and Calibration procedures were as follows:

- The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator were checked and calibrated at yearly intervals. Copies of calibration certificates are attached in **Appendix C**.

## **4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS**

4.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the ERR, the Environmental Permit and approved EM&A Programme for PHD Modification Works. The status of submission required under the Environmental Permit is summarized in **Table 4.1**. The implementation status of the environmental mitigation measures during the reporting period is summarized in **Appendix D**.

**Table 4.1 Status of Required Submissions under EP**

<b>EP Condition</b>	<b>Submission</b>	<b>Submission Date</b>
Condition 4.5	Monthly Noise Monitoring Report (February 2016)	10 <sup>th</sup> March 2016

## 5 MONITORING RESULTS

### Noise

- 5.1 In this reporting period, noise monitoring during non-restricted hours was conducted as scheduled at the designated locations. The noise monitoring schedule is shown in **Appendix E**.
- 5.2 The details of the monitoring results and graphical presentations are shown in **Appendix F**. The weather during the monitoring sessions was mainly cloudy and sunny.
- 5.3 Based on the on-site measurement, traffic on nearby major road is considered as a noise source other than construction works of the Project that affects the monitoring results of the reporting month.
- 5.4 No Action/Limit Level exceedance for construction noise monitoring was recorded in the reporting period.

### Waste Management

- 5.5 Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials and dredging materials. Non-inert C&D materials are made up of general refuse, chemical waste, paper/cardboard packaging materials, plastic materials and metals. Metals generated from the project are also grouped into non-inert C&D materials as the metals were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in **Table 5.1**. The inert C&D materials and non-inert waste generated from the Project were disposed of at TM 38 Area Fill Bank and NENT respectively. 221 kg of paper/cardboard packaging materials were generated during the reporting period. Detail of waste management data is presented in **Appendix G**.

**Table 5.1 Quantities of Waste Generated from the Project**

Reporting Month	Quantity					
	C&D Materials (inert) <sup>(a)</sup>	C&D Materials (non-inert) <sup>(b)</sup>				
		General Refuse	Chemical Waste	Paper/cardboard	Plastics	Metals
March 2016	606 m <sup>3</sup>	7 m <sup>3</sup>	0 kg	221 kg	0 kg	0 kg

Notes:

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.

(b) Non-inert C&D materials include steel, paper/cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials.

## 6 ENVIRONMENTAL SITE INSPECTION

### Site Audits

- 6.1 Site audits were carried out by ET on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix H**.
- 6.2 Site audits were conducted on 1, 8, 16, 22 and 29 March 2016 by ET. A joint site audit with the representative with IEC, ER, the Contractor and the ET was carried out on 16 March 2016. No site inspection was conducted by EPD during the reporting period. The details of observations during site audit can refer to **Table 6.1**.

### Implementation Status of Environmental Mitigation Measures

- 6.3 According to the ERR, Environmental Permit and the approved EM&A Programme of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix D**.
- 6.4 During site inspections in the reporting period, no non-conformance was identified. The observations made during the audit sessions are summarized in **Table 6.1**.



**Table 6.1 Site Audit Observations**

<b>Parameters</b>	<b>Date</b>	<b>Observations</b>	<b>Follow-up</b>
<b>Water Quality</b>	16 March 2016	<u>Observation:</u> Sediment was observed accumulated in the internal drainage channel. The Contractor was reminded to remove the sediment to well maintain the drainage system.	22 March 2016: The item was found outstanding and remarked.
	22 March 2016	<u>Observation:</u> The Contractor was reminded to clear the accumulated sediment in the U channel near the vehicle entrance in Area C and provide sand bag at the pit end.	29 March 2016: The item was found outstanding and remarked.
	29 March 2016	<u>Observation:</u> The Contractor was reminded to clear the accumulated sediment in the U channel near the vehicle entrance in Area C and provide sand bag at the pit end.	Follow up status will be provided in the next reporting month.
<b>Noise</b>	N/A	N/A	N/A
<b>Tree Protection/ Landscape and Visual</b>	24 February 2016	<u>Observation:</u> Construction material was observed stored near the existing trees at Area A. The Contractor was reminded to remove the construction material away from the tree to properly protect the tree.	The construction material was removed away from the tree.  Closing date: 1 <sup>st</sup> March 2016
<b>Air Quality</b>	24 February 2016	<u>Observation:</u> Stockpile were not covered properly at Area D, B and M100 road. The Contractor was reminded to properly cover the stockpile for dust suppression.	1 March 2016: The stockpile in M100 road was covered properly. Follow up action should be taken to the stockpile observed in Area B and D.  Closing date: 16 March 2016
	1 March 2016	<u>Observation:</u> Stockpile were not covered properly at Area D and B. The Contractor was reminded to cover the stockpile with impervious material to avoid dust generation.	8 March 2016 The stockpile in Area B was refilled, but the stock observed in Area D was found not covered.  Closing date: 16 March 2016

Parameters	Date	Observations	Follow-up
	1 March 2016	<u>Reminder:</u> The haul road in Area C and D should be provided with sufficient water spray for dust suppression.	8 March 2016 Sufficient water spray was provided to the haul road in Area C but haul road in Area D was observed dry.  Closing date: 16 March 2016
	8 March 2016	<u>Observation:</u> Stockpile was observed not covered properly in Area D. The Contractor was reminded to cover the stockpile with impervious material for dust suppression.	The stockpile in Area D was removed.  Closing date: 16 March 2016
	8 March 2016	<u>Reminder:</u> To provide sufficient water spray to the haul road in Area D.	Sufficient water spray was provided to the haul road in Area D.  Closing date: 16 March 2016
	29 March 2016	<u>Reminder:</u> To provide sufficient water spray to the haul road in area C and D.	Follow up status will be provided in the next reporting month.
<b>Waste / Chemical Management</b>	1 March 2016	<u>Observation:</u> Chemical container was observed on paved ground in Area B. The contractor was reminded to provide drip tray and remove the stagnant water and stockpile in the drip tray.	8 March 2016 The chemical drum was removed. However, the stockpile was still found in the drip tray in Area B.  Closing date: 16 March 2016
	8 March 2016	<u>Observation:</u> The Contractor was reminded to plug the drip tray observed in Area B	The drip tray was plugged and the stockpile was removed from the drip tray as well.

Parameters	Date	Observations	Follow-up
		properly, as well as remove the stockpile in the drip tray.	Closing date: 16 March 2016
	16 March 2016	<u>Observation:</u> Oil stain was observed on the paved ground at the vehicle exit in Area C. The Contractor was reminded to clear the oil stain as chemical waste.	The oil stain was cleared by the Contractor. Closing date: 22 March 2016
	16 March 2016	<u>Reminder:</u> To remove the stagnant water in the drip trays in Area B.	The stagnant water was removed. Closing date: 22 March 2016
	22 March 2016	<u>Observation:</u> Oil stain was observed on the paved ground near the vehicle entrance in Area B. The Contractor was reminded to clear the oil stain properly as chemical waste.	The oil stain was cleared by the Contractor. Closing date: 29 March 2016
	29 March 2016	<u>Observation:</u> The Contractor was reminded to provide drip tray to the oil drum found in Area C.	Follow up status will be provided in the next reporting month.
<i>Permits/ Licenses</i>	N/A	N/A	N/A

## 7 ENVIRONMENTAL NON-CONFORMANCE

### Summary of Exceedances

- 7.1 No exceedance of monitoring results was recorded in the reporting period. The summary of exceedance is provided in **Appendix I**.

### Summary of Environmental Non-Compliance

- 7.2 No environmental non-compliance was recorded in the reporting period.

### Summary of Environmental Complaint

- 7.3 No environmental Project-related complaint was received in the reporting month. The Cumulative Complaint Log since the commencement of the Project is presented in **Appendix J**.

### Summary of Environmental Summon and Successful Prosecution

- 7.4 There was no successful environmental prosecution or notification of summons received since the Project commencement. The Cumulative Log for environmental summon and successful prosecution since the commencement of the Project is presented in **Appendix J**.

## 8 FUTURE KEY ISSUES

### Key Issues in the Coming Month

8.1 Key issues to be considered in the coming month include:

- Handling of waste water arising from drilling works and surface run-off;
- Dust control during loading of materials and excavation;
- Oil leakage from equipment;
- Noise nuisance generated by on-site construction and demolition works; and
- Protection of retained trees within construction site.
- Maintaining the sand bags and bunding at the u-channel to prevent muddy run-off from directly accessing the main drainage channels.

### Monitoring Schedule for the Next Month

8.2 The tentative construction noise monitoring schedule for the next month is shown in **Appendix E**.

### Construction Programme for the Next Month

8.3 A tentative construction programme is provided in **Appendix A**. The major construction activities in the coming month will include:

- Site clearance and formation, site surveying
- Drainage works, manholes construction
- ABWF Works
- Cross track ducts construction
- Cable trough laying
- Strengthening works for OHL Mast at Location 2
- Hydroseeding
- Construction of FAO Fencing

## 9 CONCLUSIONS

### Conclusions

- 9.1 This Monthly Noise Monitoring Report presents the EM&A works undertaken during the period from 1 March to 31 March 2016 since major construction works for Contract 1117 commenced on 1 March 2013 in accordance with approved EM&A Programme for PHD Modification Works and the requirement under FEP-24/004/1998/I.
- 9.2 As of this reporting period, there is no record of any project changes from that originally proposed as described in the latest Environmental Review Report (ERR) for this Works Contract 1117.
- 9.3 No exceedance of monitoring results was recorded in the reporting period.
- 9.4 There was no environmental complaint, prosecution or notification of summons received.

- 9.5 The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

### **Recommendations**

- 9.6 The following recommendations were made in the reporting month to the Contractor during the site audits:

#### ***Water Quality***

- Internal drainage system should be well maintained.

#### ***Air Quality***

- The site should be provided with sufficient water spray for dust suppression; and
- The stockpile should be covered properly.

#### ***Waste and Chemical Management***

- Good site practice of providing drip trays for temporary use of chemicals is recommended to sustain;
- Drip trays should be properly maintained;
- Proper maintenance should be provided to equipment in site to prevent oil leakage; and

#### ***Tree Protection / Landscape and Visual***

- Avoid any construction materials, general wastes and construction wastes being stored inside the tree protection zone.


---

---

## FIGURES

---


---

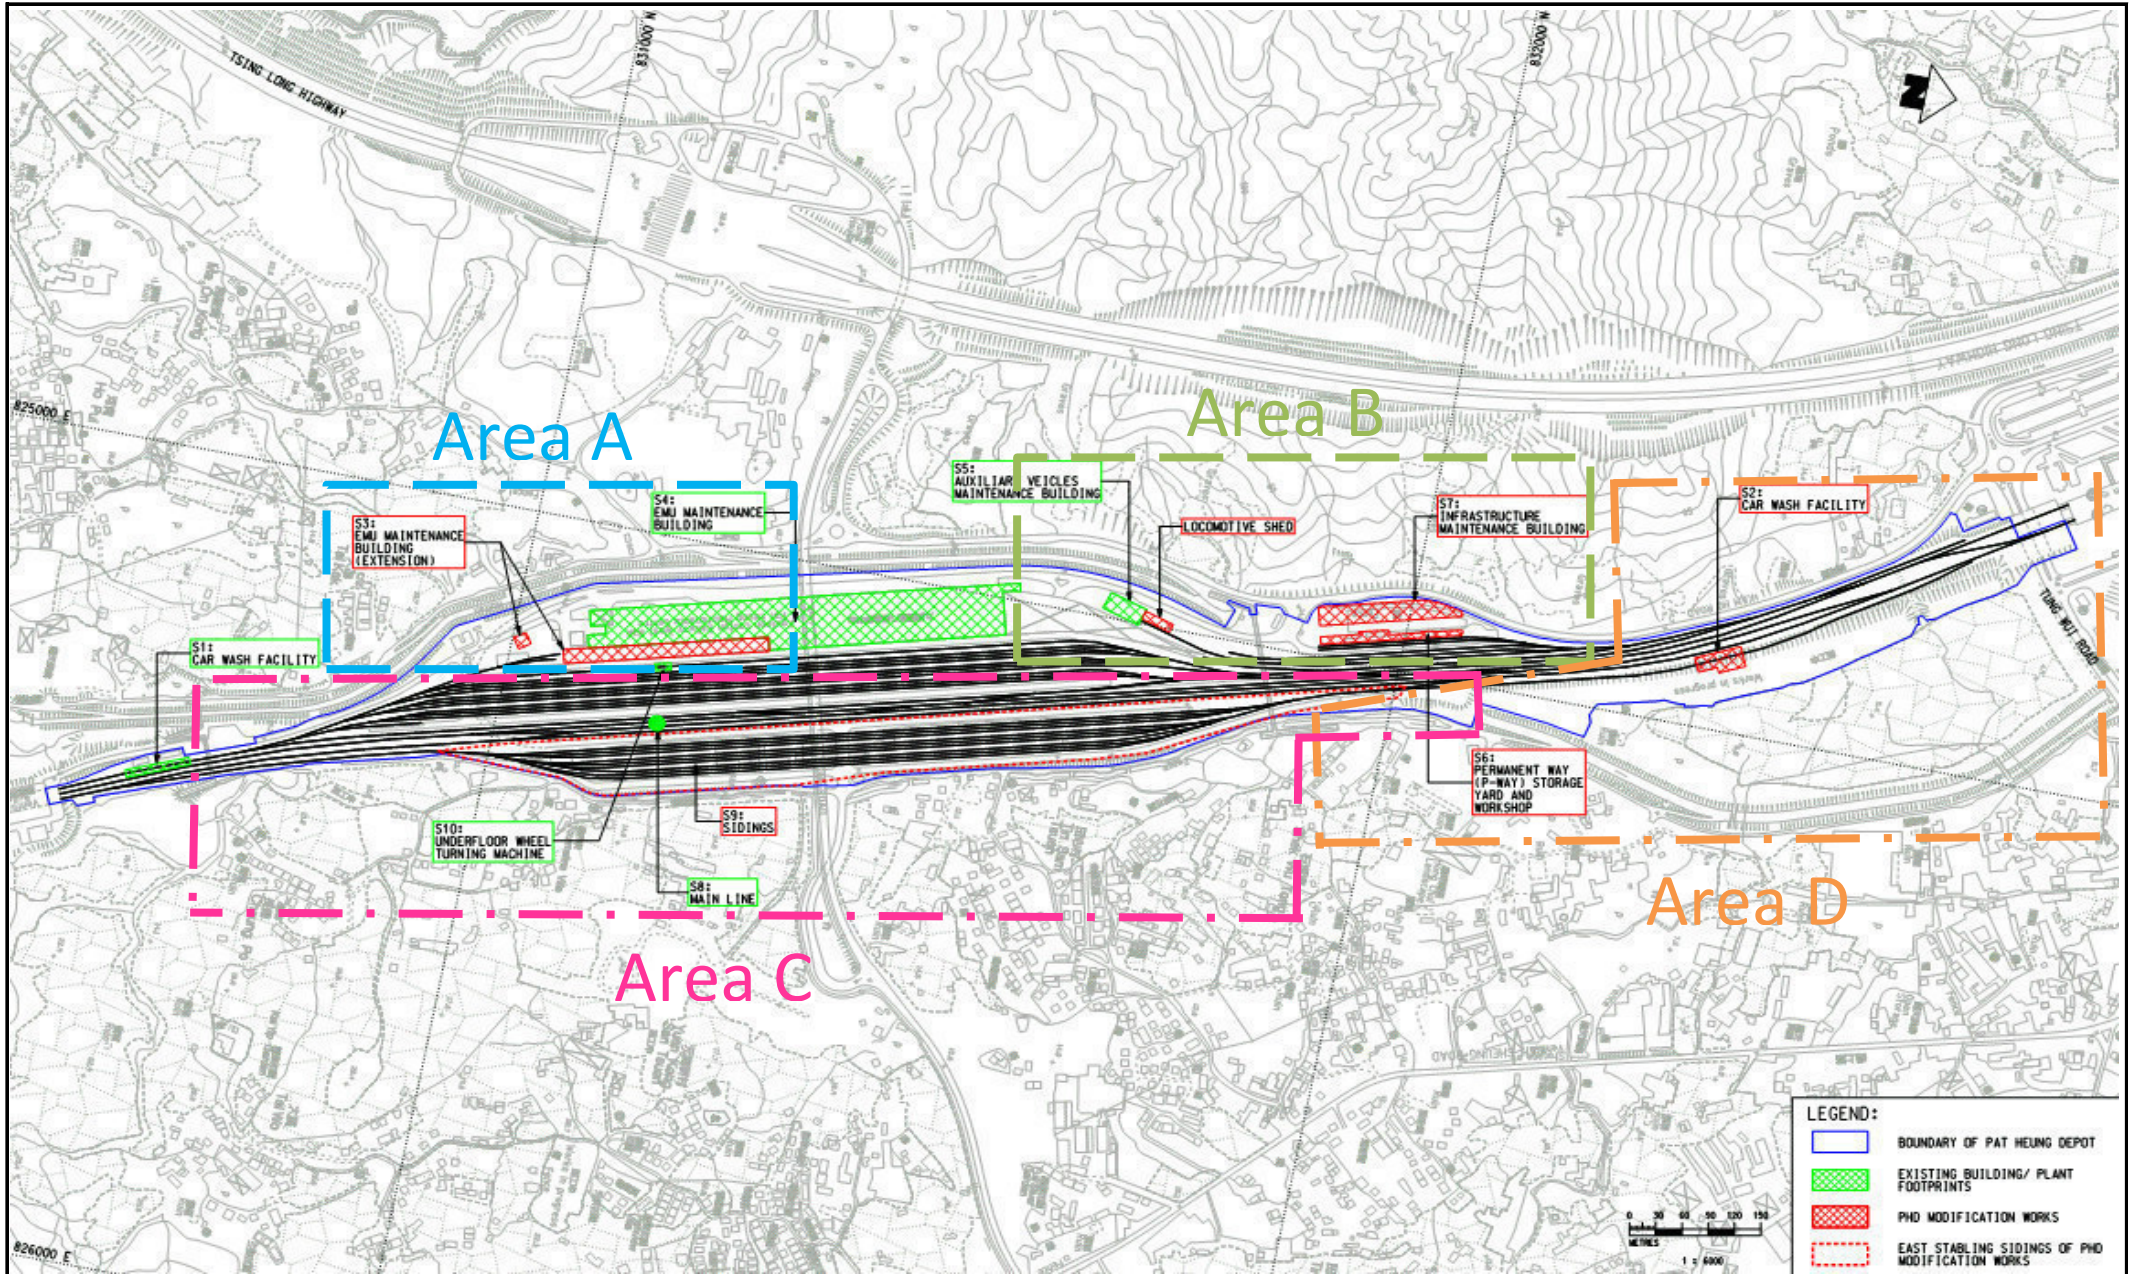

Title  
 SCL Contract 1117  
 Shatin to Central Link -  
 Pat Heung Depot Modification Works  
 Site Layout Plan

Scale	N.T.S	Proposal No.	MA13003
Date	Apr-13	Figure	1




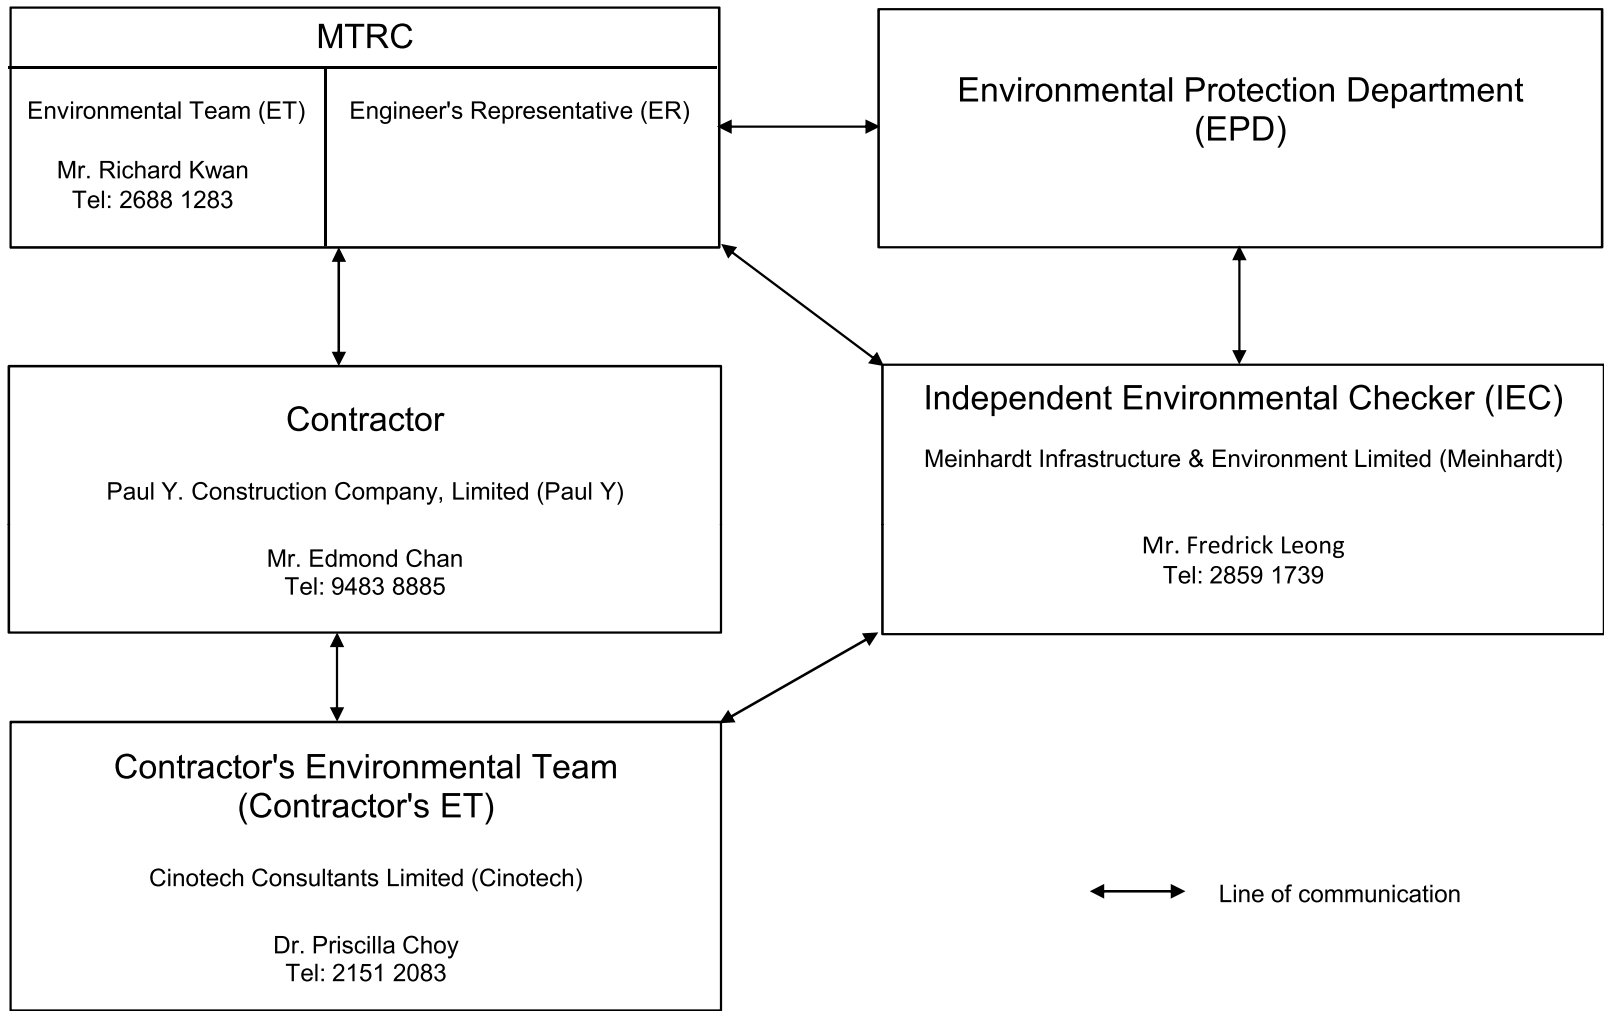

← → Line of communication

Title	SCL Contract 1117 Shatin to Central Link - Pat Heung Depot Modification Works		Scale	N.T.S	Propose	No. MA13003	CINOTECH
	Project Organisation Chart for Environmental Works		Date	Aug-13	Figure		



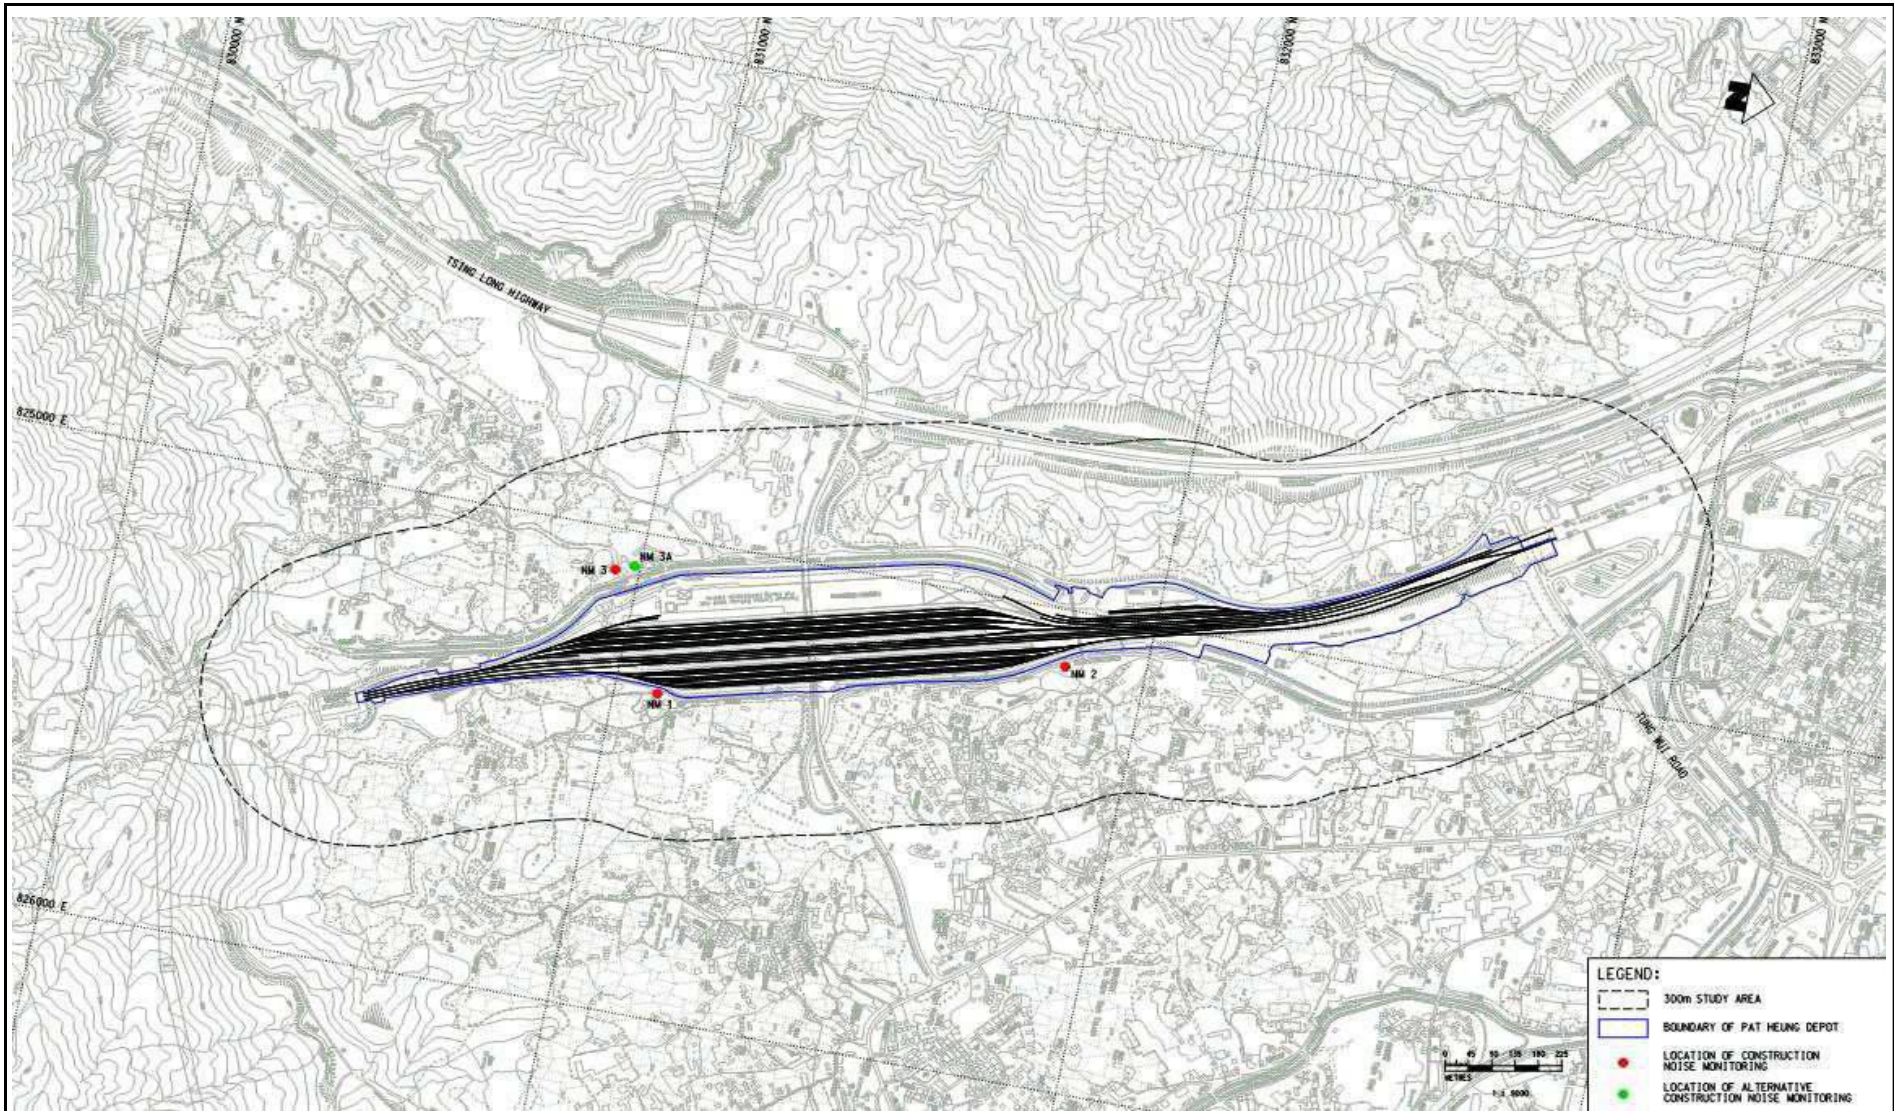

Title	MTR Works Contract 1117 Pat Heung Depot Modification Works		Scale	N.T.S	Proposal No.	MA13003	
	Location of Constrction Noise Monitoring Stations		Date	Apr-13	Figure	3	

---

---

**APPENDIX A  
TENTATIVE CONSTRUCTION  
PROGRAMME**

---

---

SCL 1117 Pat Heung Depot Modification Works

31-Dec-15

Activity ID	Activity Name	Act % Comp	Orig Dur	Rem Dur	Start	Finish	BL Early Start (PLP-000580B)	BL Early Finish (PLP-000580B)	Total Float	2013				2014				2015				2016				
										J	F	J	J	J	J	J	J	J	J	J	A	J	F	J	J	
<b>Preliminaries and General Requirements</b>																										
	Preliminaries and General Requirements		1764	669	22-Oct-12 A	29-Oct-17	31-Jul-13	29-Oct-17	0	◆																
<b>Area A - EMU Bldg Ext/Extg EMU Bldg/Noise Barrier 1/E&amp;M Ancil Bldg</b>																										
	Preliminary Works Submission (Area A)		664	0	22-Nov-12 A	23-Jul-15 A	31-Jul-13	06-Jan-14		◆																
	Materials Procurement (Area A)		333	0	29-Jan-13 A	31-Jan-15 A	31-Jul-13	15-Jul-14		◆																
	Materials Submission (Area A)		120	0	31-Dec-12 A	30-May-14 A	31-Jul-13	13-Aug-13		◆																
	Site Construction Works (Area A)		971	18	22-Oct-12 A	21-Jan-16	31-Jul-13	15-Jul-15	523	◆																
<b>EMU Building Extension</b>																										
	E0 - Geotechnical Instrumentation and Monitoring		25	0	16-Mar-13 A	19-Apr-13 A	31-Jul-13	31-Jul-13		◆																
	E0 - General Site Clearance		345	0	22-Oct-12 A	28-Feb-14 A	31-Jul-13	03-Mar-14		◆																
	E1 - Excavation and Foundation		649	0	10-Apr-13 A	31-Jul-15 A	31-Jul-13	28-Aug-14		◆																
	E2 - Civil & Structures Works		300	0	11-Apr-14 A	29-Jan-15 A	22-Feb-14	19-Aug-14		◆																
	E3 - ABWF Works		193	0	17-Oct-14 A	29-Aug-15 A	21-Jul-14	14-Feb-15		◆																
	E4 - BS Installation Works		413	18	25-Aug-14 A	21-Jan-16	21-Jul-14	05-Jun-15	229	◆																
<b>Ancillary E&amp;M Plant Building</b>																										
	E1 - Excavation and Foundation		253	0	15-Apr-13 A	09-Jun-14 A	31-Jul-13	16-Dec-13		◆																
	E2 - Civil & Structures Works		209	0	11-Jun-14 A	21-Nov-14 A	17-Dec-13	13-May-14		◆																
	E3 - ABWF Works		356	0	27-Oct-14 A	30-Jun-15 A	14-May-14	15-Jul-15		◆																
	E4 - BS Installation Works		400	3	22-May-14 A	04-Jan-16	14-May-14	14-Mar-15	245	◆																
<b>Existing EMU Building</b>																										
	Underground Drainage		30	0	20-Dec-13 A	27-Jan-14 A	20-Dec-13	27-Jan-14		◆																
	E1 - Excavation and Foundation		18	0	28-Jan-14 A	20-Feb-14 A	28-Jan-14	20-Feb-14		◆																
	E2 - Civil & Structures Works		12	0	21-Feb-14 A	06-Mar-14 A	21-Feb-14	06-Mar-14		◆																
	BS Works (Existing EMU Building) Phase A		589	0	20-Jun-13 A	24-Oct-15 A	31-Jul-13	21-Jul-14		◆																
	BS Works (Existing EMU Building) Phase B)		214	13	11-Dec-13 A	15-Jan-16	28-Jul-14	11-Dec-14	-183	◆																
<b>Miscellaneous and External Works (Overhead Line)</b>																										
	Overhead Line Construction		744	0	11-Apr-13 A	01-Apr-15 A	31-Jul-13	15-Oct-14		◆																
<b>Miscellaneous and External Works (Noise Barrier)</b>																										
	External Works near Noise Barrier (Area A)		412	0	30-Apr-14 A	06-Jul-15 A	12-Nov-13	20-Jun-14		◆																
<b>Miscellaneous and External Works (Roadworks)</b>																										
	Road Works & External Works		107	0	10-Feb-15 A	11-Apr-15 A	03-Feb-14	14-Jun-14		◆																
<b>Area B - New Fuel Station/Extg Fuel Station/New Loco Shed/New Training Track/IMB/P-Way Workshop</b>																										
	Preliminary Works Submission (Area B)		464	2	21-Nov-12 A	04-Jan-16	31-Jul-13	08-May-14	245	◆																
	Materials Procurement (Area B)		650	0	22-Oct-12 A	21-May-15 A	31-Jul-13	02-Jan-15		◆																
	Site Construction Works (Area B)		973	177	03-Dec-12 A	06-Aug-16	31-Jul-13	27-Oct-15	364	◆																
<b>Site Preparation Works</b>																										
	Works Areas W6, W6A, W6B, W6C & W6D		757	0	03-Dec-12 A	09-Feb-15 A	31-Jul-13	30-Aug-14		◆																
<b>Option 1 - MTR Cable Diversion Works</b>																										
	Systemwide Cable Diversion (Red) (Area B)		153	0	26-Apr-13 A	19-Oct-13 A	31-Jul-13	19-Oct-13		◆																
<b>Area B - New Fuel Station - Works Area W5A</b>																										
	Demolition		6	0	30-Mar-13 A	06-Apr-13 A	31-Jul-13	31-Jul-13		◆																
	Hoarding Erection (Stage 1)		6	0	12-Mar-13 A	28-Mar-13 A	31-Jul-13	31-Jul-13		◆																
	E0 - Geotechnical Instrumentation and Monitoring		12	0	01-Mar-13 A	14-Mar-13 A	31-Jul-13	31-Jul-13		◆																
	E1 - Excavation and Foundation		9	0	06-Apr-13 A	23-Apr-13 A	31-Jul-13	31-Jul-13		◆																
	E2 - Civil & Structures Works		43	0	24-Apr-13 A	31-Jul-13 A	31-Jul-13	31-Jul-13		◆																



- Remaining Level of Effort ◆ Milestone
- Actual Work ◆ Baseline Milestone
- Remaining Work
- Critical Remaining Work
- Baseline (PLP-000580B)

Revised Construction Programme (CP04Frev1) Dec 2015

Page 1 of 3  
04-Jan-16

SCL 1117 Pat Heung Depot Modification Works

Date	Revision	Checked	Approved
04-Dec-13	CP04Frev1 (updated version)		
31-Dec-15...	CP04Frev1 (RMP-1512)		



SCL 1117 Pat Heung Depot Modification Works

31-Dec-15

Activity ID	Activity Name	Act % Comp	Orig Dur	Rem Dur	Start	Finish	BL Early Start (PLP-000580B)	BL Early Finish (PLP-000580B)	Total Float	2013				2014				2015				2016			
										J	F	J	J	J	J	J	J	J	J	J	A	J	F	J	J
	Road Works at Works Area W3a (CH E1450-E1550) (Area C)		708	1	06-May-13 A	31-Dec-15	31-Jul-13	26-Jun-14	-77																
	Road Works at Works Area W3a (CH E1550-E1650) (Area C)		263	0	10-Oct-13 A	03-Sep-14 A	21-Nov-13	25-Jun-14																	
	Road Works at Works Area W3a (CH E1650-E1750) (Area C)		69	0	17-Feb-14 A	30-Sep-14 A	26-Oct-13	24-Apr-14																	
	Road Works at Works Area W3a (CH E1750-E1850) (Area C)		691	1	02-Sep-13 A	31-Dec-15	02-Sep-13	26-Jun-14	-77																
	Road Works at Works Area W3a (CH E1850-E1900) (Area C)		178	0	02-Sep-13 A	28-Mar-14 A	02-Sep-13	24-Mar-14																	
	Road Works at Works Area W3c (CH E1900-E2100) (Area C - North Fan Area)		170	0	31-Aug-13 A	10-Apr-14 A	15-Aug-13	10-Feb-14																	
	Road Works at Works Area W3c (CH E2100-E2250) (Area C - North Fan Area)		474	0	01-Mar-14 A	11-Nov-15 A	13-Sep-13	21-Feb-14																	
	Road Works at Works Area W3b (CH E1150) (Area C)		204	0	01-Oct-14 A	06-Aug-15 A	21-Jul-14	11-Dec-14																	
	Road Works at Works Area W3b (CH E1150-E1250) (Area C)		198	0	01-Oct-14 A	01-Aug-15 A	19-Jul-14	06-Dec-14																	
	Road Works at Works Area W3b (CH E1250-E1350) (Area C)		154	0	01-Oct-14 A	11-Nov-15 A	26-Jul-14	11-Dec-14																	
	<b>Area D - A100 Road Extension/Train Wash Plant &amp; Building/Noise Barrier 2 &amp; 5</b>		<b>1061</b>	<b>216</b>	<b>22-Oct-12 A</b>	<b>23-Sep-16</b>	<b>31-Jul-13</b>	<b>23-Sep-16</b>	<b>31</b>																
	Preliminary Works Submission (Area D)		772	0	09-Jan-13 A	02-Jul-15 A	31-Jul-13	26-Jul-14																	
	Materials Procurement (Area D)		76	0	22-Oct-12 A	14-Mar-14 A	31-Jul-13	20-Aug-13																	
	Materials Submission (Area D)		42	0	21-Jan-13 A	14-Mar-13 A	31-Jul-13	31-Jul-13																	
	Site Construction Works (Area D)		1024	216	21-Jan-13 A	23-Sep-16	31-Jul-13	23-Sep-16	31																
	<b>Option 1 - MTR Cable Diversion Works (A64 Drawpit)</b>		<b>303</b>	<b>0</b>	<b>03-Jun-13 A</b>	<b>15-May-14 A</b>	<b>31-Jul-13</b>	<b>16-Apr-14</b>																	
	Systemwide Cable Diversion - A64 Drawpit		303	0	03-Jun-13 A	15-May-14 A	31-Jul-13	16-Apr-14																	
	Miscellaneous and External Works (Pipe Jacking Works)		501	0	14-Jun-13 A	31-Oct-14 A	31-Jul-13	14-Jun-14																	
	Pipe Jacking (North) (Area D)		501	0	14-Jun-13 A	31-Oct-14 A	31-Jul-13	14-Jun-14																	
	Miscellaneous and External Works (Overhead Line)		674	40	11-Nov-13 A	20-Feb-16	11-Nov-13	22-Jun-15	206																
	OHL Reprovision adjacent to WRL Main Line (Area D)		674	40	11-Nov-13 A	20-Feb-16	11-Nov-13	22-Jun-15	206																
	Miscellaneous and External Works (Train Wash Facility)		787	216	17-Feb-14 A	23-Sep-16	17-Feb-14	23-Sep-16	31																
	E1 - Excavation and Foundation		157	0	17-Feb-14 A	19-Aug-14 A	17-Feb-14	02-May-14																	
	E2 - Civil & Structures Works		293	0	23-Jul-14 A	15-Apr-15 A	03-May-14	24-Jul-14																	
	E3 - ABWF Works		193	28	27-Dec-14 A	02-Feb-16	28-Jul-14	24-Apr-15	191																
	E4 - BS Installation Works		415	216	07-Oct-14 A	23-Sep-16	30-Jul-14	23-Sep-16	2																
	Miscellaneous and External Works (Noise Barrier)		824	10	22-Apr-13 A	12-Jan-16	31-Jul-13	22-Jun-15	237																
	Noise Barrier (Area D)		824	10	22-Apr-13 A	12-Jan-16	31-Jul-13	22-Jun-15	237																
	Miscellaneous and External Works (Tree Management)		114	0	21-Jan-13 A	23-Jul-13 A	31-Jul-13	31-Jul-13																	
	Tree Management (Area D)		114	0	21-Jan-13 A	23-Jul-13 A	31-Jul-13	31-Jul-13																	
	Miscellaneous and External Works (Fill Embankment)		308	0	01-Apr-13 A	09-Aug-14 A	31-Jul-13	09-Mar-14																	
	Fill Embankment Works		308	0	01-Apr-13 A	09-Aug-14 A	31-Jul-13	09-Mar-14																	
	Miscellaneous and External Works (Roadworks)		568	95	30-May-14 A	28-Apr-16	17-Feb-14	15-Oct-14	152																
	A100 Access Road Extension (Area D)		568	95	30-May-14 A	28-Apr-16	17-Feb-14	15-Oct-14	152																



- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline (PLP-000580B)
- Milestone
- Baseline Milestone

Revised Construction Programme (CP04Frev1) Dec 2015

SCL 1117 Pat Heung Depot Modification Works

Date	Revision	Checked	Approved
04-Dec-13	CP04Frev1 (updated version)		
31-Dec-15...	CP04Frev1 (RMP-1512)		

---

---

**APPENDIX B**  
**EVENT AND ACTION PLAN**

---

---

**Event and Action Plan for Noise Monitoring during Construction Phase**

Event	Action			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> <li>1. Notify IEC, Contactor, and ER;</li> <li>2. Discuss with the ER, IEC, and Contractor on remedial measures required; and</li> <li>3. Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the investigation results submitted by the contractor; and</li> <li>2. Review and advise the ET and ER on the effectiveness of the remedial measures proposed by the Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor, IEC and ET;</li> <li>3. Review and agree on the remedial measures proposed by the Contractor; and</li> <li>4. Supervise implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Investigate the complaint and propose remedial measures;</li> <li>2. Report the results of investigation to the IEC, ET and ER;</li> <li>3. Submit noise mitigation proposals to ER with copy to the IEC and ET within 3 working days of notification; and</li> <li>4. Implement noise mitigation proposals.</li> </ol>
Limit Level	<ol style="list-style-type: none"> <li>1. Notify IEC, EPD and Contractor;</li> <li>2. Repeat measurement to confirm findings;</li> <li>3. Increase monitoring frequency;</li> <li>4. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>5. Arrange meeting with the IEC, Contractor and ER to discuss the remedial measures to be taken;</li> <li>6. Inform IEC, ER, EPD the causes and actions taken for the exceedances; and</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by the ET;</li> <li>2. Check the Contractor's working method;</li> <li>3. Discuss with the ER, ET, and Contractor on the potential remedial measures; and</li> <li>4. Review and advise the ET and ER on the effectiveness of the remedial measures proposed by the Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor, IEC and ET;</li> <li>3. In consultation with the ER and IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures; and</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify source and investigate the causes of exceedance;</li> <li>2. Take immediate action to avoid further exceedance;</li> <li>3. Submit proposals for remedial actions to ER with copy to IEC and ET within 3 working days;</li> <li>4. Implement the agreed proposals;</li> <li>5. Revise and resubmit proposals if problem still not under control; and</li> <li>6. Stop the relevant portion of works as determined by the ER until the exceedance is abated</li> </ol>

---

---


**APPENDIX C  
COPIES OF CALIBRATION  
CERTIFICATES**

---

---



the sound investment



# Model 105 & 106

## Acoustic Calibrators

- Advanced performance ensures that both models meet or exceed IEC 60942 accuracy requirements
- Ergonomic and robust design
- Auto correction for temperature and barometric pressure
- Auto switch-off in normal mode and 'permanent-on' mode available
- Low battery indicator
- 94dB Sound Pressure Level
- Fits 1/2 inch international standard microphones
- 1/4 inch microphone adapter available



The Models 105 & 106 are part of the NEW generation of Pulsar Instruments acoustic calibrators that allow you to quickly check the accuracy of your sound level meter or dosimeter thus complying with International regulations and codes of practice.

Great care has been taken during the design process to ensure that the units are comfortable to hold, robust and easy to use, whilst performing accurately throughout a wide range of temperature, humidity and pressure conditions.

In use they fit over the microphone of the instrument and produce a stable 1kHz tone at 94dB, the frequency and sound level respectively, as mandated by the standard.

The Model 105 meets the precision of Class 1 of IEC 60942, while the lower cost Model 106 meets industrial Class 2.

The calibrators are powered by an easy to access single 9 volt battery giving many months or even years of operation. An automatic shut-off circuit ensures power conservation should you forget to switch the unit off after calibrating.



綜合試驗有限公司  
SOILS & MATERIALS ENGINEERING CO., LTD.

G/F, 9/F, 12/F, 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下·9樓·12樓·13樓及20樓  
E-mail: smec@cigismec.com Website: www.cigismec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



## CERTIFICATE OF CALIBRATION

Certificate No.: 15CA0518 02-02 Page: 1 of 2

### Item tested

Description: Acoustical Calibrator (Class 1)  
Manufacturer: Pulsar Instruments Ltd.  
Type/Model No.: Model 105  
Serial/Equipment No.: 51342  
Adaptors used: -

### Item submitted by

Customer: Paul Y. General Contractors Limited  
Address of Customer: -  
Request No.: -  
Date of receipt: 18-May-2015

Date of test: 20-May-2015

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	15-Apr-2016	SCL
Preamplifier	B&K 2673	2743150	22-Apr-2016	CEPREI
Measuring amplifier	B&K 2610	2346941	22-Apr-2016	CEPREI
Signal generator	DS 360	61227	16-Apr-2016	CEPREI
Digital multi-meter	34401A	US36087050	17-Apr-2016	CEPREI
Audio analyzer	8903B	GB41300350	17-Apr-2016	CEPREI
Universal counter	53132A	MY40003662	16-Apr-2016	CEPREI

### Ambient conditions

Temperature: 21 ± 1 °C  
Relative humidity: 60 ± 10 %  
Air pressure: 1000 ± 5 hPa

### Test specifications


- 1, The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- 2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using Insert voltage technique.
- 3, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013,25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

### Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.


Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:

  
Huang Jian-Min/Feng Jun Qi

Date: 21-May-2015

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

15CA0518 02-02

Page: 2 of 2

### 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	(Output level in dB re 20 $\mu$ Pa)
			Estimated Expanded Uncertainty dB
1000	94.00	93.77	0.10

### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz STF = 0.003 dB

Estimated expanded uncertainty 0.005 dB

### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz Actual Frequency = 1000.1 Hz

Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz TND = 0.6 %

Estimated expanded uncertainty 0.7%

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95 %. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by:

Date: 20-May-2015

Fung Chi Yip

Checked by:

Date: 21-May-2015

Lam Tzo Wai

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

SVAN

Head office. ✓



綜合試驗有限公司  
SOILS & MATERIALS ENGINEERING CO., LTD.

G/F, 9/F, 12/F, 13/F & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@cigsmecc.com Website: www.cigsmecc.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



## CERTIFICATE OF CALIBRATION

Certificate No.: 15CA0518 02-01 Page 1 of 2

### Item tested

Description:	Sound Level Meter (Type 1)	Microphone
Manufacturer:	SVANTEK, POLAND	ACO, JAPAN
Type/Model No.:	955	7052E
Serial/Equipment No.:	27455	50002
Adaptors used:	-	-

### Item submitted by

Customer Name: Paul Y. General Contractors Limited  
Address of Customer: -  
Request No.: -  
Date of receipt: 18-May-2015

Date of test: 20-May-2015

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound callibrator	B&K 4226	2288444	20-Jun-2015	CIGSMEC
Signal generator	DS 360	33873	16-Apr-2016	CEPREI
Signal generator	DS 360	61227	16-Apr-2016	CEPREI

### Ambient conditions

Temperature: 20 ± 1 °C  
Relative humidity: 60 ± 10 %  
Air pressure: 1000 ± 5 hPa

### Test specifications

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsiveness of the Sound Level Meter.

### Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.


Actual Measurement data are documented on worksheets.

Approved Signatory:

  
Huang Jiarui/Feng Jun Qi

Date: 21-May-2015

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



綜合試驗有限公司  
SOILS & MATERIALS ENGINEERING CO., LTD.

G/F, 9/F, 12/F, 13/F. & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下·9樓·12樓·13樓及20樓  
E-mail: smec@clgismec.com Website: www.clgismec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 15CA0518 02-01 Page 2 of 2

### 1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertainty (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
	C	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Frequency weightings	A	Pass	0.3
Time weightings	C	Pass	0.3	
	Lin	Pass	0.3	
	Single Burst Fast	Pass	0.3	
Peak response	Single Burst Slow	Pass	0.3	
	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
	Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3
Time averaging	Repeated at frequency of 100 Hz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
	Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertainty (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

### 3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by:

Fung Chi Yip

Date: 20-May-2015

Checked by:

Lam Tze Wal

Date: 21-May-2015

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



綜合試驗有限公司  
SOILS & MATERIALS ENGINEERING CO., LTD.

G/F, 9/F, 12/F, 13/F, & 20/F, Leader Centre, 37 Wong Chuk Hong Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@clgismec.com Website: www.clgismec.com

Tel : (852) 2875 6860  
Fax : (852) 2556 7533



A CIGIS GROUP COMPANY

Test Data for Sound Level Meter

Page 1 of 5

Sound level meter type: 955 Serial No. 27455 Date 20-May-2015  
Microphone type: 7052E Serial No. 50002 Report: 15CA0518 02-01

SELF GENERATED NOISE TEST

The noise test is performed in the most sensitive range of the SLM with the microphone replaced by an equivalent impedance.

Noise level in A weighting < 25.0 dB  
Noise level in C weighting < 25.0 dB  
Noise level in Lin < 25.0 dB

LINEARITY TEST

The linearity is tested relative to the reference sound pressure level using a continuous sinusoidal signal of frequency 4 kHz. The measurement is made on the reference range for indications at 5 dB intervals starting from the 94 dB reference sound pressure level. And until within 5 dB of the upper and lower limits of the reference range, the measurements shall be made at 1 dB intervals. (SLM set to LEQ/SPL)

Reference/Expected level	Actual level		Tolerance	Deviation	
	non-integrated	Integrated		non-Integrated	Integrated
dB	dB	dB	+/- dB	dB	dB
94.0	94.0	94.0	0.7	0.0	0.0
99.0	99.0	99.0	0.7	0.0	0.0
104.0	104.0	104.0	0.7	0.0	0.0
109.0	109.0	109.0	0.7	0.0	0.0
114.0	114.0	114.0	0.7	0.0	0.0
119.0	119.0	119.0	0.7	0.0	0.0
124.0	124.0	124.0	0.7	0.0	0.0
129.0	129.0	129.0	0.7	0.0	0.0
134.0	134.0	134.0	0.7	0.0	0.0
135.0	135.0	135.0	0.7	0.0	0.0
136.0	136.0	136.0	0.7	0.0	0.0
137.0	137.0	137.0	0.7	0.0	0.0
138.0	138.0	138.0	0.7	0.0	0.0
139.0	139.0	139.0	0.7	0.0	0.0
140.0	140.0	140.0	0.7	0.0	0.0
89.0	89.0	89.0	0.7	0.0	0.0
84.0	84.0	84.0	0.7	0.0	0.0
79.0	79.0	79.0	0.7	0.0	0.0
74.0	74.0	74.0	0.7	0.0	0.0
69.0	69.0	69.0	0.7	0.0	0.0
64.0	64.0	64.0	0.7	0.0	0.0
59.0	59.0	59.0	0.7	0.0	0.0
54.0	54.0	54.0	0.7	0.0	0.0
49.0	49.0	49.0	0.7	0.0	0.0
44.0	43.9	43.9	0.7	-0.1	-0.1



**綜合試驗有限公司**  
**SOILS & MATERIALS ENGINEERING CO., LTD.**

G/F, 9/F, 12/F, 13/F & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@cigismec.com Website: www.cigismec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



A CIGIS GROUP COMPANY

Test Data for Sound Level Meter

Page 2 of 5

Sound level meter type: 955 Serial No. 27455 Date 20-May-2015  
Microphone type: 7052E Serial No. 50002

Report: 15CA0518 02-01

39.0	38.9	38.9	0.7	-0.1	-0.1
34.0	33.9	33.9	0.7	-0.1	-0.1
29.0	28.7	28.7	0.7	-0.3	-0.3
28.0	27.6	27.6	0.7	-0.4	-0.4
27.0	26.5	26.5	0.7	-0.5	-0.5
26.0	25.4	25.4	0.7	-0.6	-0.6

Measurements for an indication of the reference SPL on all other ranges which include it

Other ranges	Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
25-140	94.0	94.0	0.7	0.0

Measurements on all level ranges for indications 2 dB below the upper limit and 2 dB above the lower limit

Ranges	Reference/Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
25-140	27.0	26.5	0.7	-0.5
	138.0	138.0	0.7	0.0

**FREQUENCY WEIGHTING TEST**

The frequency response of the weighting networks are tested at octave intervals over the frequency ranges 31.5 Hz to 12500 Hz. The signal level at 1000 Hz is set to give an indication of the reference SPL.

Frequency weighting A:

Frequency Hz	Ref. level dB	Expected level dB	Actual level dB	Tolerance(dB)		Deviation dB
				+	-	
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	54.6	54.6	1.5	1.5	0.0
63.1	94.0	67.8	67.8	1.5	1.5	0.0
125.9	94.0	77.9	77.9	1.0	1.0	0.0
251.2	94.0	85.4	85.3	1.0	1.0	-0.1
501.2	94.0	90.8	90.7	1.0	1.0	-0.1
1995.0	94.0	95.2	95.1	1.0	1.0	-0.1
3981.0	94.0	95.0	95.0	1.0	1.0	0.0
7943.0	94.0	92.9	92.9	1.5	3.0	0.0
12590.0	94.0	89.7	89.6	3.0	6.0	-0.1

Frequency weighting C:


Frequency Hz	Ref. level dB	Expected level dB	Actual level dB	Tolerance(dB)		Deviation dB
				+	-	
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	91.0	91.0	1.5	1.5	0.0
63.1	94.0	93.2	93.1	1.5	1.5	-0.1



**綜合試驗有限公司**  
**SOILS & MATERIALS ENGINEERING CO., LTD.**

G/F., 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@ciglsmec.com Website: www.ciglsmec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



A CIGIS GROUP COMPANY

Test Data for Sound Level Meter

Page 3 of 5

Sound level meter type: 955 Serial No. 27455 Date 20-May-2015  
Microphone type: 7052E Serial No. 50002 Report: 15CA0518 02-01

125.9	94.0	93.8	93.8	1.0	1.0	0.0
251.2	94.0	94.0	93.9	1.0	1.0	-0.1
501.2	94.0	94.0	94.0	1.0	1.0	0.0
1995.0	94.0	93.8	93.8	1.0	1.0	0.0
3981.0	94.0	93.2	93.2	1.0	1.0	0.0
7943.0	94.0	91.0	91.0	1.5	3.0	0.0
12590.0	94.0	87.8	87.7	3.0	6.0	-0.1

Frequency weighting Lin:

Frequency Hz	Ref. level dB	Expected level dB	Actual level dB	Tolerance(dB)		Deviation dB
				+	-	
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	94.0	93.9	1.5	1.5	-0.1
63.1	94.0	94.0	93.9	1.5	1.5	-0.1
125.9	94.0	94.0	93.9	1.0	1.0	-0.1
251.2	94.0	94.0	94.0	1.0	1.0	0.0
501.2	94.0	94.0	93.9	1.0	1.0	-0.1
1995.0	94.0	94.0	93.9	1.0	1.0	-0.1
3981.0	94.0	94.0	93.9	1.0	1.0	-0.1
7943.0	94.0	94.0	93.9	1.5	3.0	-0.1
12590.0	94.0	94.0	93.9	3.0	6.0	-0.1

TIME WEIGHTING FAST TEST

Time weighting F is tested on the reference range with a single sinusoidal burst of duration 200 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level dB	Expected level dB	Actual level dB	Tolerance(dB)		Deviation dB
			+	-	
127.0	126.0	126.0	1.0	1.0	0.0

TIME WEIGHTING SLOW TEST

Time weighting S is tested on the reference range with a single sinusoidal burst of duration 500 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level dB	Expected level dB	Actual level dB	Tolerance(dB)		Deviation dB
			+	-	
127.0	122.9	122.9	1.0	1.0	0.0

PEAK RESPONSE TEST

The onset time of the peak detector is tested on the reference range by comparing the response to a 100 us rectangular test pulse with the response to a 10 ms reference pulse of the same amplitude. The amplitude of the 10 ms reference pulse is such as to produce an indication 1 dB below the upper limit of the primary indicator range. Positive polarities: (Weighting C, set the generator signal to single, Lcpmax)





**綜合試驗有限公司**  
SOILS & MATERIALS ENGINEERING CO., LTD.

G/F, 9/F, 12/F, 13/F & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@clgismec.com Website: www.clgismec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533



A CIGIS GROUP COMPANY

Test Data for Sound Level Meter

Page 4 of 5

Sound level meter type: 955 Serial No. 27455 Date 20-May-2015  
Microphone type: 7052E Serial No. 50002

Report: 15CA0518 02-01

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
130.0	130.0	129.8	2.0	-0.2

Negative polarities:

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
130.0	130.0	129.8	2.0	-0.2

**RMS ACCURACY TEST**

The RMS detector accuracy is tested on the reference range for a crest factor of 3.

Test frequency: 2000 Hz  
Amplitude: 2 dB below the upper limit of the primary indicator range.  
Burst repetition frequency: 40 Hz  
Tone burst signal: 11 cycles of a sine wave of frequency 2000 Hz. (Set to INT)

Time weighting	Ref. Level	Expected level	Tone burst signal	Tolerance	Deviation
	dB	dB	indication(dB)	+/- dB	dB
Slow	129.0+6.6	129.0	129.0	0.5	0.0

**TIME WEIGHTING IMPULSE TEST**

Time weighting I is tested on the reference range (Set the SLM to LAImax)

Test frequency: 2000 Hz  
Amplitude: The upper limit of the primary indicator range.

Single sinusoidal burst of duration 5 ms;

Ref. Level	Single burst indication		Tolerance	Deviation
	Expected (dB)	Actual (dB)		
131.0	122.2	122.2	2.0	0.0

Repeated at 100 Hz

Ref. Level	Repeated burst indication		Tolerance	Deviation
	Expected (dB)	Actual (dB)		
131.0	128.3	128.2	1.0	-0.1

**TIME AVERAGING TEST**

This test compares the SLM reading for continuous sine signals with readings obtained from a sine tone burst sequence having the same RMS level. The test level is 30 dB below the upper limit of the linearity range and repeated for Type 1 SLM with 40 dB below the upper limit of the linearity.

Frequency of tone burst: 4000 Hz

Duration of tone burst: 1 ms

Repetition Time	Level of tone burst	Expected Leq	Actual Leq	Tolerance	Deviation	Remarks
msec	dB	dB	dB	+/- dB	dB	
1000	108.0	108.0	107.9	1.0	-0.1	60s integ.
10000	98.0	98.0	97.9	1.0	-0.1	6min. integ.

**PULSE RANGE AND SOUND EXPOSURE LEVEL TEST**



**綜合試驗有限公司**  
**SOILS & MATERIALS ENGINEERING CO., LTD.**

G/F, 9/F, 12/F, 13/F & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.  
香港黃竹坑道37號利達中心地下, 9樓, 12樓, 13樓及20樓  
E-mail: smec@clgismec.com Website: www.clgismec.com

Tel : (852) 2873 6860  
Fax : (852) 2555 7533

  
A CIGIS GROUP COMPANY

Test Data for Sound Level Meter

Page 5 of 5

Sound level meter type: 955 Serial No. 27455 Date 20-May-2015  
Microphone type: 7052E Serial No. 50002  
Report: 15CA0518 02-01

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency: 4000 Hz

Integration time: 10 sec

The integrating sound level meter set to Leq:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10	85.0	55.0	55.0	1.7	0.0

The Integrating sound level meter set to SEL:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10.0	85.0	65.0	65.0	1.7	0.0

OVERLOAD INDICATION TEST

For SLM capable of operating in a non-integrating mode.

Test frequency: 2000 Hz

Amplitude: 2 dB below the upper limit of the primary indicator range.

Burst repetition frequency: 40 Hz

Tone burst signal: 11 cycles of a sine wave of frequency 2000 Hz.

Level	Level reduced by	Further reduced	Difference	Tolerance	Deviation
at overload (dB)	1 dB	3 dB	dB	dB	dB
135.0	134.0	131.0	3.0	1.0	0.0

For integrating SLM, with the instrument indicating Leq.

For integrating SLM, with the instrument indicating Leq and set to the reference range. The test signal as follow

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency: 4000 Hz

Integration time: 10 sec

Single burst duration: 1 msec

Rms level	Level reduced by	Expected level	Actual level	Tolerance	Deviation
at overload (dB)	1 dB	dB	dB	dB	dB
140.9	139.9	99.9	99.9	2.2	0.0

ACOUSTIC TEST

The acoustic test of the complete SLM is tested at the frequency 125 Hz and 8000 Hz using a B&K type 4226 Multifunction Acoustic Calibrator. The test is performed in A weighting.

Frequency	Expected level	Actual level	Tolerance (dB)		Deviation
			+	-	
Hz	dB	Measured (dB)			dB
1000	94.0	94.0	0.0	0.0	0.0
125	77.9	77.9	1.0	1.0	0.0
8000	92.9	93.9	1.5	3.0	1.0

-----END-----

---

---

**APPENDIX D  
UPDATED ENVIRONMENTAL  
MITIGATION IMPLEMENTATION  
SCHEDULE**

---

---

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
<b><i>Ecology (Construction Phase)</i></b>			
S7.6.2	-	<p><u>Tree Felling and Vegetation Clearance</u></p> <p>Tree felling and compensatory planting will be implemented in accordance with the requirements of ETWB TCW No. 3/2006 as far as practicable.</p> <p><u>Water Quality</u></p> <p>Good construction site practices as required in ProPECC PN1/94 will be followed as appropriate. Implementation of some good construction practices are presented as follows:</p> <ul style="list-style-type: none"> <li>• Containment of silt runoff within the site boundary;</li> <li>• Appropriate storage and disposal of chemicals and chemical waste and the provision of sanitary facilities for on-site workers;</li> <li>• Erection of temporary geo-textile silt or sediment fences/oil traps around any earth-moving works to trap any sediments and prevent them from entering watercourses;</li> <li>• Avoidance of soil storage against trees or close to water bodies;</li> <li>• No on-site burning of waste; and;</li> <li>• Waste and refuse in appropriate receptacles.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>
<b><i>Landscape &amp; Visual (Construction Phase)</i></b>			
S9.11	-	<p>The following good site practices and measures have been recommended:</p> <ul style="list-style-type: none"> <li>• Re-use of Existing topsoil and fill generated from site</li> <li>• For soil conservation, existing topsoil shall be re-used where possible for new planting areas within the project. The construction program shall consider using the soil removed from one phase for backfilling another. Suitable storage ground, gathering ground and mixing ground may be set up on-site as necessary.</li> <li>• To maximise protection to existing trees, ground vegetation and the associated under storey habitats, construction contracts may designate “No-intrusion Zone” to various areas within the site boundary with rigid and durable fencing for each individual no-intrusion zone. The contractor should closely monitor and restrict the site working staff from entering the “no-intrusion zone”, even for indirect construction activities and storage of equipment.</li> <li>• All retained trees should be recorded photographically at the commencement of the Contract, and carefully protected during the construction period. Detailed tree protection specification shall be allowed for and included in the Contract Specification, which specifies the tree protection requirement, submission and approval system, and the tree monitoring system,</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p>

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> <li>In addition, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works sites.</li> </ul>	^
Table 9.7	CM1	<u>Site Hoarding</u> Erection of solid screen during construction stage to prevent undesirable views of the construction site from visually sensitive areas.	^
Table 9.7	CM2	<u>Management of facilities on work sites</u> To provide proper site management of the facilities on the sites, give control on the height and disposition/ arrangement of all welfare facilities and construction plant on site to minimise landscape and visual impacts to adjacent VSRs and existing/retained site features.	^
Table 9.7	CM3	<u>Construction programme</u> Employ construction techniques which assist in streamlining construction programme, minimise the duration of plant operations. Consider prefabrication of building elements offsite to minimise on site works and construction period.	^
<b><i>Air Quality</i></b>			
-	-	<u>Emission from Vehicles and Plants</u> <ul style="list-style-type: none"> <li>All vehicles shall be shut down in intermittent use.</li> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke.</li> <li>All diesel fuelled construction plant within the works areas shall be powered by ultra-low sulphur diesel fuel (ULSD)</li> </ul>	^ ^ ^
<b><i>Construction Dust Impact</i></b>			
S6.3.3	-	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation potential dust impacts. 8-time watering per day on exposed worksites is recommended during construction phase to further alleviate the potential construction dust impacts.	#
S6.3.3	-	<ul style="list-style-type: none"> <li>Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;</li> <li>Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;</li> <li>A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones.</li> <li>The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from</li> </ul>	* ^ ^ ^

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		<p>the vehicle;</p> <ul style="list-style-type: none"> <li>• Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcore;</li> <li>• When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing; Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;</li> <li>• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;</li> <li>• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;</li> <li>• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;</li> <li>• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;</li> <li>• Any skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>N/A<sup>(2)</sup></p> <p>^</p> <p>^</p>
<b><i>Construction Airborne Noise</i></b>			
S5.5.6	-	<p>Implement the following good site practices:</p> <ul style="list-style-type: none"> <li>• Louvres should be orientated away from adjacent NSRs, preferably onto the main line of WRL which are less sensitive.</li> <li>• Direct noise mitigation measures including silencers, acoustic louvers and acoustic enclosures should be allowed for in the design for the maintenance buildings, plant buildings and workshops.</li> <li>• The façade and doors for these plant / workshops would have adequate sound insulation properties to minimise the noise emanating through the building fabric to acceptable level.</li> </ul>	<p>N/A<sup>(2)</sup></p> <p>N/A<sup>(2)</sup></p> <p>^</p>

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> <li>Acoustic treatments such as silencer, acoustic louvers, noise barriers and acoustic enclosures should be installed for the existing equipment where necessary to minimise the cumulative noise impacts on the NSRs.</li> </ul>	^
<b>Water Quality (Construction Phase)</b>			
S12.5	-	<p>In accordance with the Practice Noise for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following:</p> <p><u>Construction Runoff and Site Drainage</u></p> <ul style="list-style-type: none"> <li>At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction.</li> <li>The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates.</li> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1m<sup>3</sup>/s a sedimentation basin of 30m<sup>3</sup> would be required and for a flow rate of 0.5 m<sup>3</sup>/s the basin would be 150 m<sup>3</sup>. The detailed design of the sand/silt traps shall be undertaken by the Contractor prior to the commencement of construction.</li> <li>All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means.</li> <li>The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows.</li> <li>All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and</li> </ul>	<p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">N/A<sup>(2)</sup></p> <p style="text-align: center;">^</p> <p style="text-align: center;">N/A<sup>(2)</sup></p> <p style="text-align: center;">#</p>

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		<p>particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.</p> <ul style="list-style-type: none"> <li>• Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.</li> <li>• Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m<sup>3</sup> should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.</li> <li>• Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.</li> <li>• Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes.</li> <li>• All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.</li> <li>• Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain.</li> </ul>	<p style="text-align: right;">^</p> <p style="text-align: right;">^</p> <p style="text-align: right;">^</p> <p style="text-align: right;">N/A<sup>(2)</sup></p> <p style="text-align: right;">^</p> <p style="text-align: right;">N/A<sup>(2)</sup></p>
S12.5.1.2	-	<p><u>Sewage Effluent</u></p> <ul style="list-style-type: none"> <li>• Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.</li> </ul>	<p style="text-align: right;">^</p>
S12.5.1.3	-	<p><u>Accidental Spillage</u></p> <ul style="list-style-type: none"> <li>• In order to prevent accidental spillage of chemicals, proper storage and handling facilities should be provided. All the tanks, containers, storage area should be banded</li> </ul>	<p style="text-align: right;">#</p>



## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		and the locations should be locked as far as possible from the sensitive watercourse and storm water drains. The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings. Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste disposal (Chemical Waste) (General) Regulation.	
<b>Waste Management (Construction Waste)</b>			
S11.5.1	-	<ul style="list-style-type: none"> <li>A trip-ticket system should be established and will comply with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation to monitor the disposal of public fill and solid wastes at public filling facilities and landfills, and to control fly-tipping.</li> </ul>	^
S11.5.1	-	<p><u>C &amp; D Material</u></p> <ul style="list-style-type: none"> <li>Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement;</li> <li>Carry out on-site sorting;</li> <li>Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate;</li> <li>Adopt “Selective Demolition” technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible;</li> <li>Implement a trip-ticket system for each works contract to ensure that the disposal of C&amp;D materials are properly documented and verified; and</li> <li>Implement an enhanced Waste Management Plan, which become a part of the Environmental Management Plan in accordance with “ETWBTC (Works) No. 19/2005 – Waste Management on Construction Site”, to encourage on-site sorting of C&amp;D materials and to minimize their generation during the course of construction.</li> <li>In addition, disposal of the C&amp;D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation.</li> </ul>	^ ^ ^ N/A <sup>(2)</sup> ^ ^ ^
S11.5.1	-	<p><u>C&amp;D Waste</u></p> <ul style="list-style-type: none"> <li>Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&amp;D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage.</li> <li>The Contractor should recycle as much of the C&amp;D materials as possible on-site. Public fill and C&amp;D waste should be segregated and stored in different containers or</li> </ul>	^ ^

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.	
S11.5.1	-	<p><u>General Refuse</u></p> <ul style="list-style-type: none"> <li>• General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.</li> <li>• Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible.</li> <li>• Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. In addition, waste separation facilities for paper, aluminium cans, plastic bottles etc., should be provided.</li> </ul>	<p>^</p> <p>^</p> <p>^</p>
S11.5.1	-	<p><u>Chemical Waste</u></p> <p>Chemical waste producers should be registered with EPD. For those processes which generate chemical waste, the Contractor shall identify any alternatives that generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste.</p> <p>Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows.</p> <p>Containers used for storage of chemical wastes should:</p> <ul style="list-style-type: none"> <li>• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>• Have a capacity of less than 450 L unless the specification have been approved by EPD; and</li> <li>• Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations.</li> </ul> <p>The storage area for chemical wastes should:</p> <ul style="list-style-type: none"> <li>• Be clearly labelled and used solely for the storage of chemical wastes;</li> <li>• Be enclosed on at least 3 sides;</li> <li>• Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest;</li> </ul>	<p>^</p> <p>N/A<sup>(2)</sup></p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>

## Appendix D - MTR Works Contract 1117–Summary of Environmental Mitigation Implementation Schedule

ERR <sup>(1)</sup> Ref.	ID No.	Recommended Mitigation Measures	Status
		<ul style="list-style-type: none"> <li>• Have adequate ventilation;</li> <li>• Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste, if necessary); and</li> <li>• Be arranged so that incompatible materials are adequately separated.</li> </ul> <p>Disposal of chemical waste should:</p> <ul style="list-style-type: none"> <li>• Be via a licensed waste collector; and</li> <li>• Be to a facility licensed to receive chemical waste, such as the CWTC which also offers a chemical waste collection service and can supply the necessary storage containers; or</li> <li>• Be to a re-user of the waste, under approval from EPD.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>N/A<sup>(2)</sup></p>

Remarks:

(1) The latest Environmental Review Report (ERR) for Pat Heung Depot Modification Works is referred in preparation of this summary.

^ Compliance of mitigation measure                      X                      Non-compliance of mitigation measure

- Non-compliance but rectified by the contractor

- \* Recommendation was made during site audit but improved/rectified by the contractor.

- # Recommendation was made during site audit but not yet improved/rectified by the contractor.

N/A<sup>(1)</sup> Not Applicable

N/A<sup>(2)</sup> Not Applicable at this stage

---

---

**APPENDIX E  
ENVIRONMENTAL MONITORING  
SCHEDULE**

---

---

Contract No. SCL 1117  
 Pat Heung Depot Modification Works  
 Impact Noise Monitoring Schedule for March 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Mar	2-Mar	3-Mar	4-Mar	5-Mar
6-Mar	7-Mar	8-Mar	9-Mar	10-Mar	11-Mar	12-Mar
	Noise (1) at NM1, NM2 & NM3A					
13-Mar	14-Mar	15-Mar	16-Mar	17-Mar	18-Mar	19-Mar
	Noise (1) at NM1, NM2 & NM3A					
20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar
	Noise (1) at NM1, NM2 & NM3A					
27-Mar	28-Mar	29-Mar	30-Mar	31-Mar		
		Noise (1) at NM1, NM2 & NM3A				

**Noise Monitoring Station:**

NM1 - Tourmaline Villa  
 NM2 - Kam Po Road  
 NM3A - Tai Kek Tsuen

Category	Time Period
(1)	0700-1900 hrs on normal weekdays

Contract No. SCL 1117  
 Pat Heung Depot Modification Works  
 Tentative Impact Noise Monitoring Schedule for April 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1-Apr	2-Apr
3-Apr	4-Apr	5-Apr	6-Apr	7-Apr	8-Apr	9-Apr
		Noise (1) at NM1, NM2 & NM3A				
10-Apr	11-Apr	12-Apr	13-Apr	14-Apr	15-Apr	16-Apr
			Noise (1) at NM1, NM2 & NM3A			
17-Apr	18-Apr	19-Apr	20-Apr	21-Apr	22-Apr	23-Apr
	Noise (1) at NM1, NM2 & NM3A					
24-Apr	25-Apr	26-Apr	27-Apr	28-Apr	29-Apr	30-Apr
	Noise (1) at NM1, NM2 & NM3A					

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Noise Monitoring Station:**

NM1 - Tourmaline Villa  
 NM2 - Kam Po Road  
 NM3A - Tai Kek Tsuen

Category	Time Period
(1)	0700-1900 hrs on normal weekdays

---

---

**APPENDIX F  
NOISE MONITORING RESULTS AND  
GRAPHICAL PRESENTATIONS**

---

---

## Appendix F - Noise Monitoring Results




Location NM1 - Tourmaline Villa							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
7-Mar-16	9:51	Cloudy	63.7	61.9	47.1	61.2	60.1
14-Mar-16	9:45	Cloudy	58.3	55.2	48.4		58.3 Measured ≤ Baseline
21-Mar-16	13:50	Cloudy	59	60	45.9		59 Measured ≤ Baseline
29-Mar-16	14:43	Sunny	55.5	53.4	44.4		55.5 Measured ≤ Baseline

Location NM2 - Kam Po Road							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
7-Mar-16	10:35	Cloudy	61.7	65.9	47.7	61.3	51.1
14-Mar-16	10:26	Cloudy	59.8	58.1	48.1		59.8 Measured ≤ Baseline
21-Mar-16	13:06	Cloudy	57.7	57.9	47.9		57.7 Measured ≤ Baseline
29-Mar-16	15:21	Sunny	61.2	61.3	47.6		61.2 Measured ≤ Baseline

Location NM3A - Tai Kek Tsuen							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
7-Mar-16	9:03	Cloudy	64.9	64.8	50.7	66.7	64.9 Measured ≤ Baseline
14-Mar-16	8:57	Cloudy	63.5	63.4	57.3		63.5 Measured ≤ Baseline
21-Mar-16	14:39	Cloudy	63.4	60.1	52.9		63.4 Measured ≤ Baseline
29-Mar-16	13:58	Sunny	62.5	58.7	53.1		62.5 Measured ≤ Baseline



## Noise Levels

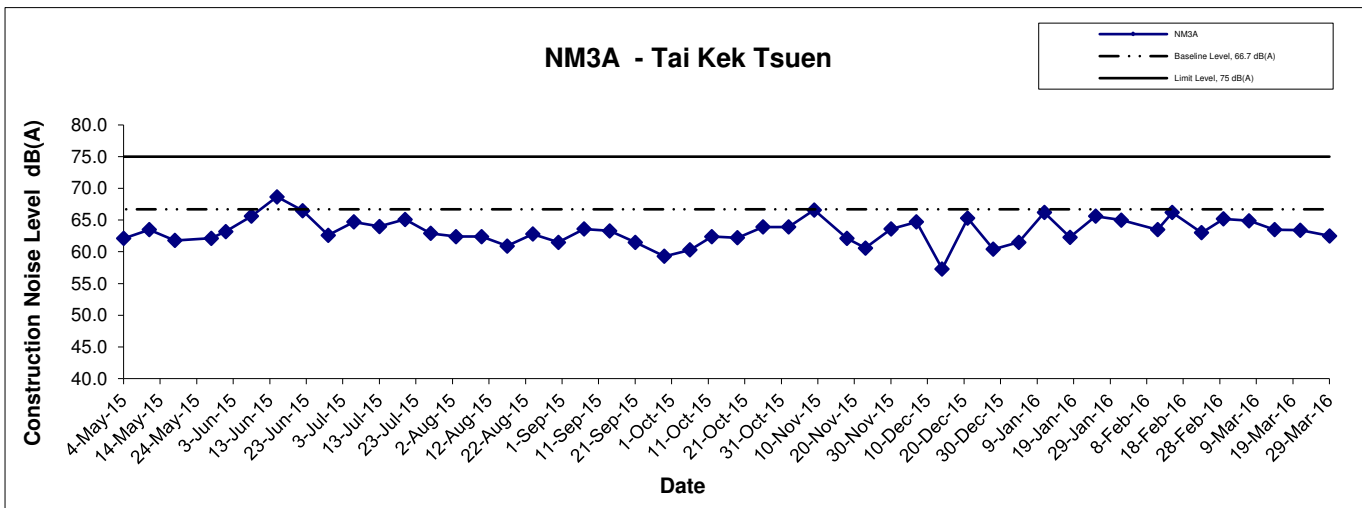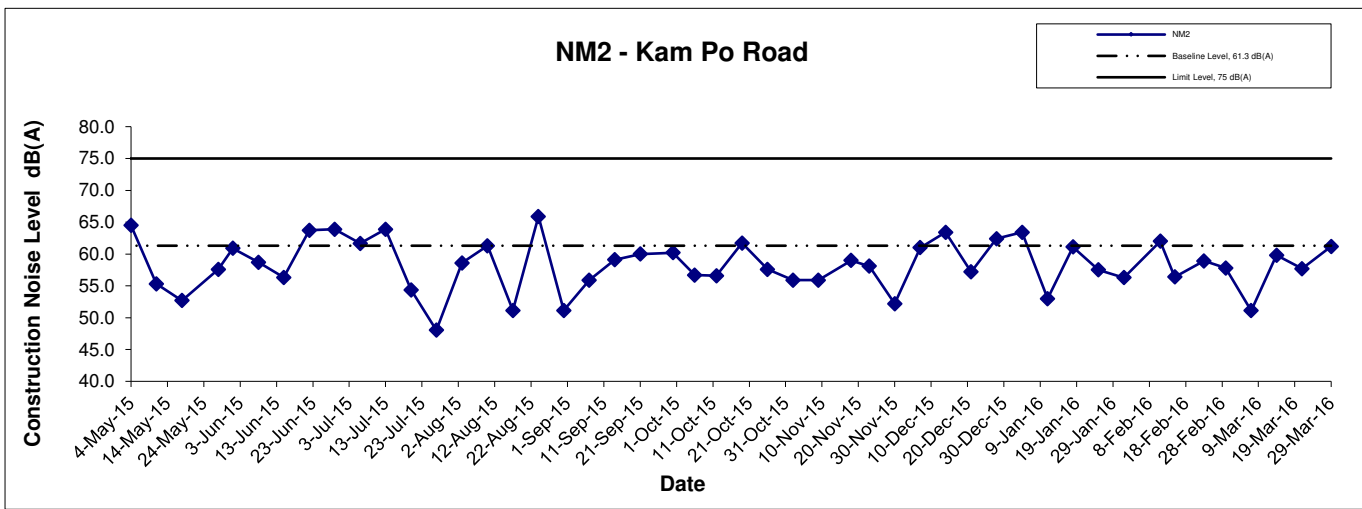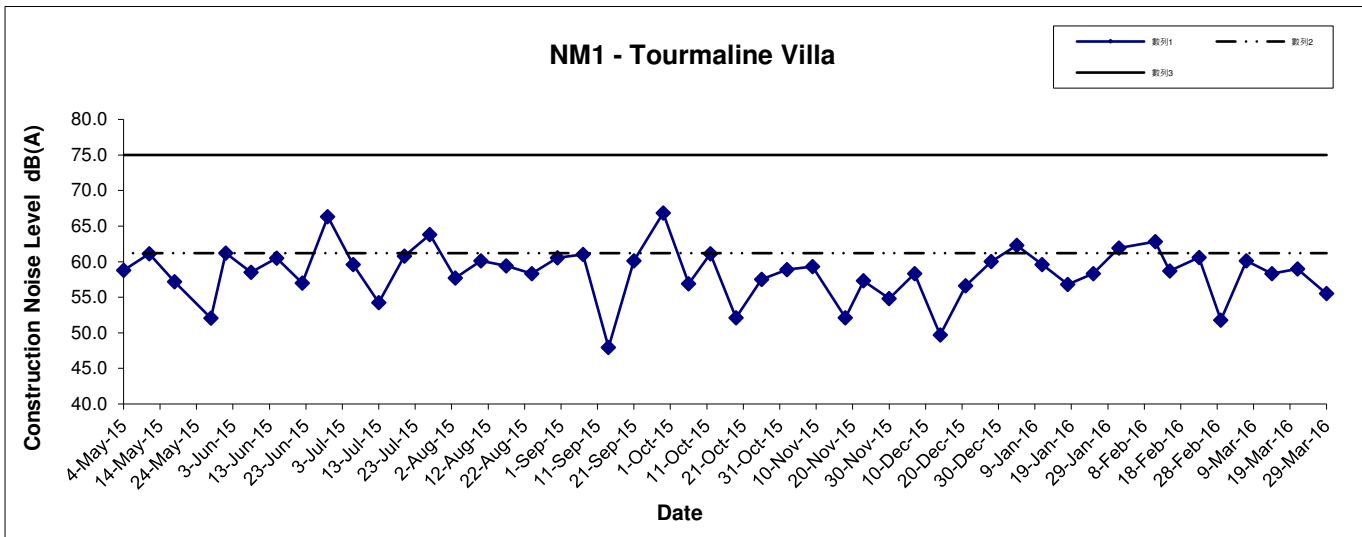

Title MTR Works Contract 1117 Pat Heung Depot Modification Works Graphical Presentation of the Construction Noise Monitoring Results	Scale	N.T.S	Project No.	MA13003	CINOTECH
	Date	Mar-15	Appendix	F	

---

---

**APPENDIX G  
WASTE GENERATION IN THE  
REPORTING MONTH**

---

---

**Paul Y. Construction Company, Limited**  
**MTR Contract 1117**  
**Pat Heung Depot Modification Works**

**Monthly Summary Waste Flow Table for 2016 (year)**

Month	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed to Sorting Facilities	Disposed to Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in kg)	(in kg)	(in kg)	(in '000m <sup>3</sup> )
Jan '16	0.162	-	-	-	0.000	0.162	-	-	340	-	-	0.020
Feb '16	0.398	-	-	-	0.010	0.388	-	2.07	274	-	-	0.000
Mar '16	0.606	-	-	-	0.003	0.603	-	-	221	-	-	0.007
Apr '16												
May '16												
Jun '16												
Sub-total	1.166				0.013	1.153		2.070	835			0.028
Jul '16												
Aug '16												
Sep '16												
Oct '16												
Nov '16												
Dec '16												
Total	1.166				0.013	1.153		2.070	835.000			0.028

Note:

Assume the densities of Rock, Soil, Mix Rock and Soil are Regular Spoil to be 2.0 tonnes/m<sup>3</sup>. Assumption the densities of general refuse is 1.0 tonnes/m<sup>3</sup>

---

---

**APPENDIX H  
SITE AUDIT SUMMARY**

---

---

**Shatin to Central Link -  
Contract 1117 Pat Heung Depot Modification Works**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	160301
Date	1 March 2016 (Tuesday)
Time	0900-1130

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
160301-001	<p><b>Part B - Water Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part C - Tree Management Protection / Landscape &amp; Visual Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>Stockpile were not covered properly at Area D and B. The Contractor was reminded to cover the stockpile with impervious material to avoid dust generation.</li> </ul>	D 7
160301-R03	<ul style="list-style-type: none"> <li>The haul road in Area C and D should be provided with sufficient water spray for dust suppression.</li> </ul> <p><b>Part E - Construction Noise Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul>	D 6
160301-002	<p><b>Part F - Waste/Chemical Management</b></p> <ul style="list-style-type: none"> <li>Chemical container was observed on paved ground in Area B. The contractor was reminded to provide drip tray and remove the stagnant water and stockpile in the drip tray.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:160224), the item 160224-002 was remarked as 160301-001 and will be reviewed in the next inspection.</li> </ul>	F 9

	Name	Signature	Date
Recorded by	Benjamin Wong		1 March 2016
Checked by	Dr. Priscilla Choy		1 March 2016

**Shatin to Central Link -  
Contract 1117 Pat Heung Depot Modification Works**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	160308
Date	8 March 2016 (Tuesday)
Time	0900-1130

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
160308-O02	<p><b>Part B - Water Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul>	D 7
160308-R03	<p><b>Part C - Tree Management Protection / Landscape &amp; Visual Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>Stockpile was observed not covered properly in Area D. The Contractor was reminded to cover the stockpile with impervious material for dust suppression.</li> <li>To provide sufficient water spray to the haul road in Area D.</li> </ul>	D 6
160308-O01	<p><b>Part E - Construction Noise Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste/Chemical Management</b></p> <ul style="list-style-type: none"> <li>The Contractor was reminded to plug the drip tray observed in Area B properly, as well as remove the stockpile in the drip tray.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:160301), the item 160301-O01, 160301-O02 and 160301-R03 were remarked as 160308-O02, 160308-O01 and 160308-R03 respectively and will be reviewed in the next inspection.</li> </ul>	F 9

	Name	Signature	Date
Recorded by	Benjamin Wong		8 March 2016
Checked by	Dr. Priscilla Choy		8 March 2016

//

**Shatin to Central Link -  
Contract 1117 Pat Heung Depot Modification Works**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	160316
Date	16 March 2016 (Wednesday)
Time	1400-1600

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
160316-002	<p><b>Part B - Water Quality</b></p> <ul style="list-style-type: none"> <li>Sediment was observed accumulated in the internal drainage channel. The Contractor was reminded to remove the sediment to well maintain the drainage system.</li> </ul>	B 8
160316-001	<p><b>Part C - Tree Management Protection / Landscape &amp; Visual Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part E - Construction Noise Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste/Chemical Management</b></p> <ul style="list-style-type: none"> <li>Oil stain was observed on the paved ground at the vehicle exit in Area C. The Contractor was reminded to clear the oil stain as chemical waste.</li> </ul>	F 8
160316-R03	<ul style="list-style-type: none"> <li>To remove the stagnant water in the drip trays in Area B.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:160308), all the environmental deficiencies were improved/ rectified by the Contractor.</li> </ul>	F 9

	Name	Signature	Date
Recorded by	Benjamin Wong		16 March 2016
Checked by	Dr. Priscilla Choy		16 March 2016

**Shatin to Central Link -  
Contract 1117 Pat Heung Depot Modification Works**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	160322
Date	22 March 2016 (Wednesday)
Time	0900-1100

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
160322-002	<p><b>Part B - Water Quality</b></p> <ul style="list-style-type: none"> <li>The Contractor was reminded to clear the accumulated sediment in the U channel near the vehicle entrance in Area C and provide sand bag at the pit end.</li> </ul>	B 8
160322-001	<p><b>Part C - Tree Management Protection / Landscape &amp; Visual Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part E - Construction Noise Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste/Chemical Management</b></p> <ul style="list-style-type: none"> <li>Oil stain was observed on the paved ground near the vehicle entrance in Area B. The Contractor was reminded to clear the oil stain properly as chemical waste.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:160316), the item 160316-002 was remarked as 160322-002 and will be reviewed in the next inspection.</li> </ul>	F 8

	Name	Signature	Date
Recorded by	Benjamin Wong		22 March 2016
Checked by	Dr. Priscilla Choy		22 March 2016



**Shatin to Central Link -**

**Contract 1117 Pat Heung Depot Modification Works**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	160329
Date	29 March 2016 (Wednesday)
Time	0900-1100

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
160329-O02	<p><b>Part B - Water Quality</b></p> <ul style="list-style-type: none"> <li>The Contractor was reminded to clear the accumulated sediment in the U channel near the vehicle entrance in Area C and provide sand bag at the pit end.</li> </ul>	B 8
160329-R03	<p><b>Part C - Tree Management Protection / Landscape &amp; Visual Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part D - Air Quality</b></p> <ul style="list-style-type: none"> <li>To provide sufficient water spray to the haul road in area C and D.</li> </ul>	D 6
160329-O01	<p><b>Part E - Construction Noise Impact</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part F - Waste/Chemical Management</b></p> <ul style="list-style-type: none"> <li>The Contractor was reminded to provide drip tray to the oil drum found in Area C.</li> </ul> <p><b>Part G - Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>No environmental deficiency was identified during the site inspection.</li> </ul> <p><b>Part H - Remark</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:160322), the item 160322-O02 was remarked as 160329-O02 and will be reviewed in the next inspection.</li> </ul>	F 9

	Name	Signature	Date
Recorded by	Benjamin Wong		29 March 2016
Checked by	Dr. Priscilla Choy		29 March 2016

---

---

**APPENDIX I  
SUMMARY OF EXCEEDANCE**

---

---

**APPENDIX I – SUMMARY OF EXCEEDANCE**

**Reporting Month:** March 2016

*a) Exceedance Report for Noise Monitoring (NIL)*

---

---

**APPENDIX J  
CUMULATIVE LOG FOR COMPLAINTS,  
NOTIFICATIONS OF SUMMONS AND  
SUCCESSFUL PROSECUTIONS**

---

---

**Appendix J - Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions**

**Cumulative Complaint Log**

Log Ref.	Date/Location	Complainant/ Date of Contact	Details of Complaint	Investigation/ Mitigation Action	File Closed
--	--	--	--	--	--

**Cumulative Log for Notifications of Summons**

Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since project commencement
--	--	--	--	--	--

**Cumulative Log for Successful Prosecutions**

Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since the commencement of the project
--	--	--	--	--	--
