



JOB No.: TCS01216/21

**WSD Contract No.: 3/WSD/20 -
Reclaimed Water Supply to Sheung Shui and Fanling**

**MONTHLY ENVIRONMENTAL MONITORING & AUDIT
REPORT (NO.3) – FEBRUARY 2022**

**PREPARED FOR
WATER SUPPLIES DEPARTMENT**

Quality Index

Date	Reference No.	Prepared By	Approved By
10 March 2022	TCS01216/21/600/R0026v1	 Martin Li Environmental Consultant	 TW Tam Environmental Team Leader

Version	Date	Description
1	10 March 2022	First Submission



NATURE & TECHNOLOGIES (HK) LIMITED

科 技 環 保 (香 港) 有 限 公 司

Lot 12, Tam Kon Shan Road, North Tsing Yi, New Territories, Hong Kong

香港新界北青衣担杆山路 12 號地段

Tel 電話: (852) 2877 3122

Fax 傳真: (852) 2511 0922

Email 電郵: enquiry@nt.com.hk Website 網址: <http://www.nt.com.hk>

Date: 14th March 2022

Project Manager
Water Supplies Department
Immigration Tower, 7 Gloucester Road,
Wan Chai, Hong Kong
Attn: Mr. Freeman Kei

Dear Sir,

Agreement No. CE67/2017(WS)

Reclaimed Water Supply to Sheung Shi and Fanling – Investigation, Design and Construction

Independent Environmental Checker (IEC) Services for

Shek Wu Hui Water Reclamation Plant under Contract No. 3/WSD/20

Monthly EM&A Monitoring Report for February 2022

We refer to the monthly EM&A Report for February 2022 for WSD Contract No.: 3/WSD/20 – Reclaimed Water Supply to Sheung Shui and Fanling certified by the Environmental Team Leader on 14th March 2022. Please note we have no adverse comments on the captioned submission. The captioned submission is hereby verified in accordance with the requirement stipulated in Condition 3.4 of Environmental Permit No. FEP-01/470/2013.

Should you have any query, please feel free to contact the undersigned at 2877 3122 or at 6113 2368 (vegawong@nt.com.hk).

Yours Sincerely,

For and on behalf of

Nature & Technologies (HK) Limited

Vega Wong

Independent Environmental Checker

c.c.

- ET Leader -- AUES (Attn: Mr. T.W. Tam) [by Email: twtam@fordbusiness.com]
- Resident Engineer – Binnies Hong Kong Limited (Attn: Mr. Chester Chan) [by Email: chancw@binnies.com]

EXECUTIVE SUMMARY

- ES.01 Water Supplies Department (WSD) is the Project Proponent and the Permit Holder of **Reclaimed Water Supply to Sheung Shui and Fanling** (hereinafter referred as “the Contract Works”), which is a Designated Project to be implemented under Further Environmental Permit number FEP-01/470/2013 (hereinafter referred as “the FEP-01/470/2013” or “the FEP”).
- ES.02 In according with the Updated EM&A Manual stipulation and the location of Contract Works, only construction noise monitoring and waterbird of ecological monitoring are required during the construction phase of the Contract Works.
- ES.03 As part of the EM&A programme, Baseline Monitoring Report which determined Action and Limit Levels (A/L Levels) based on the baseline data, has been verified by Independent Environmental Checker (IEC) and submitted to EPD endorsement on **24 November 2021**. Also, construction activities under the Contract Works were commenced on **7 December 2021**.
- ES.04 This is the **3rd** monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1** to **28 February 2022** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES.06 Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Table ES-1 Environmental monitoring activities in the Reporting Period

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Total Occasions during Reporting Period
Construction Noise	$L_{eq(30min)}$ Daytime	4
Ecology	Waterbirds	4
Site Inspection / Audit	ET, the Contractor and RE joint site Environmental Inspection	4

BREACH OF ACTION AND LIMIT (A/L) LEVELS

- ES.07 In the Reporting Period, no construction noise limit level exceedance construction noise was recorded and no noise complaint (i.e. Action Level) was received. No action and limit level exceedance for waterbirds survey was recorded in the Reporting Period. No Notifications of Exceedances (NOEs) was issued to the Resident Engineer (RE), IEC and the Main Contractor. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Table ES-2 Breach of Action and Limit (A/L) Levels in the Reporting Period

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	0	0
Ecology	Waterbirds Abundance	0	0	0	0	0

ENVIRONMENTAL COMPLAINT

- ES.08 No environmental complaint was recorded or received in this Reporting Month. The statistics of environmental complaint are summarized in the following table.

Table ES-3 Environmental Complaint Summaries in the Reporting Month

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

- ES.09 In addition, no complaints received and emergency events relating to violation of environmental legislation for illegal dumping and landfilling were received.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

- ES.10 No environmental summons or successful prosecution was recorded in this Reporting Month. The statistics of summons or successful prosecutions are summarized in the following tables.

Table ES-4 Environmental Summons Summaries in the Reporting Month

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

Table ES-5 Environmental Prosecution Summaries in the Reporting Month

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

REPORTING CHANGE

- ES.11 No reporting change was made in the Reporting Period.

SITE INSPECTION

- ES.12 Weekly site inspections to evaluate the site environmental performance have been carried out by the RE, ET and the Main Contractor on **4, 10, 18 and 23 February 2022**. No non-compliance was noted during the site inspection. Additional, no site visit was undertaken by EPD or AFCD within the Reporting Period.

FUTURE KEY ISSUES

- ES.13 In coming month, piling works will be ongoing underway. Therefore, construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants or mobile noise barriers should be implemented in accordance with the EM&A requirement.
- ES.14 Raining season will come soon. To prevent muddy water or other water pollutants via site surface water runoff get into the rivers, mitigation measures such as temporary draining or wastewater treatment systems shall be to provide.
- ES.15 Moreover, the Contractor shall fully implement mitigation measures prevent dust emission.

TABLE OF CONTENTS

1.	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	REPORT STRUCTURE	1
2.	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.1	PROJECT ORGANIZATION	2
2.2	CONSTRUCTION PROGRESS	3
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	3
3.	SUMMARY OF IMPACT MONITORING REQUIREMENTS	4
3.1	GENERAL	4
3.2	REQUIREMENT OF CONSTRUCTION NOISE MONITORING	4
3.3	LOCATION OF CONSTRUCTION NOISE IMPACT MONITORING	4
3.4	EVENT AND ACTION PLAN	4
3.5	NOISE MONITORING METHODOLOGY	5
3.6	MONITORING PROCEDURE	5
3.7	DATA MANAGEMENT AND DATA QA/QC CONTROL	5
3.8	REQUIREMENT OF WATERBIRDS ECOLOGICAL IMPACT MONITORING	6
3.9	EVENT ACTION PLAN	7
4.	CONSTRUCTION NOISE MONITORING	9
4.1	GENERAL	9
4.2	RESULTS OF NOISE MONITORING	9
5.	ECOLOGY WATERBIRD MONITORING	10
5.1	GENERAL	10
5.2	RESULTS OF WATERBIRDS SURVEY	10
6.	WASTE MANAGEMENT	12
6.1	GENERAL WASTE MANAGEMENT	12
6.2	RECORDS OF WASTE QUANTITIES	12
7.	SITE INSPECTION	13
7.1	REQUIREMENTS	13
7.2	FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	13
8.	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	14
8.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	14
9.	IMPLEMENTATION STATUS OF MITIGATION MEASURES	15
9.1	GENERAL REQUIREMENTS	15
9.2	TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	15
9.3	KEY ISSUES FOR THE COMING MONTH	15
10.	CONCLUSIONS AND RECOMMENDATIONS	16
10.1	CONCLUSIONS	16
10.2	RECOMMENDATIONS	16

LIST OF TABLES

TABLE 2-3-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-4-1	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-5-1	EQUIPMENT OF NOISE IMPACT MONITORING
TABLE 3-8-1	MONITORING OF MEASURES TO MINIMIZE DISTURBANCE TO WATERBIRDS ON THE NG TUNG, SHEUNG YUE AND SHEK SHEUNG RIVERS
TABLE 3-9-1	ECOLOGICAL MONITORING STATIONS
TABLE 3-10-1	EVENT AND ACTION PLAN FOR CONSTRUCTION NOISE MONITORING
TABLE 3-10-2	EVENT AND ACTION PLAN OF ECOLOGICAL (WATERBIRDS) MONITORING
TABLE 4-2-1	SUMMARIES OF NOISE MONITORING RESULTS OF CP-KTN-NMS5
TABLE 5-1-1	REPRESENTATIVE WATERBIRDS
TABLE 5-2-1	TOTAL BIRD SPECIES AND ABUNDANCE IN THE REPORTING MONTH
TABLE 5-2-2	ABUNDANCE OF REPRESENTATIVE WATERBIRDS IN THE REPORTING MONTH
TABLE 6-2-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 6-2-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 7-2-1	SITE OBSERVATIONS
TABLE 8-1-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-1-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-1-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LOCATION OF SHEK WU HUI WATER RECLAMATION PLANT
APPENDIX B	PROJECT ORGANIZATION
APPENDIX C	MASTER CONSTRUCTION PROGRAM
APPENDIX D	DESIGNATED NOISE MONITORING STATION LOCATION
APPENDIX E	VALID CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT
APPENDIX F	MONITORING SCHEDULE OF THE REPORTING MONTH AND COMING MONTH
APPENDIX G	DATABASE OF MONITORING RESULT
APPENDIX H	GRAPHICAL PLOTS FOR MONITORING RESULT
APPENDIX I	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX J	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)
APPENDIX K	WATERBIRDS SURVEY REPORT FOR THE REPORTING MONTH

1. INTRODUCTION**1.1 BACKGROUND**

- 1.1.1 Water Supplies Department (WSD) is the Project Proponent of Utilization of Treated Sewage Effluent (TSE) from Shek Wu Hui Sewage Treatment Works. On 30th July 2021, China Geo-Engineering Corporation (hereinafter named as “the Main-Contractor”) was awarded WSD Contract Works 3/WSD/20 - Reclaimed Water Supply to Sheung Shui and Fanling (hereinafter referred as “the Contract Works”).
- 1.1.2 The major work of the Contract Works is to construct the Shek Wu Hui Water Reclamation Plant. Location of Shek Wu Hui Water Reclamation Plant is shown in [Appendix A](#). For the Contract Works, Shek Wu Hui Water Reclamation Plant construction is a Designated Project to be implemented under Further Environmental Permit number FEP-01/470/2013 (hereinafter referred as “the FEP-01/470/2013” or “the FEP”).
- 1.1.3 Pursuant to the FEP stipulation, the Main Contractor has commissioned Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) as Environmental Team (hereinafter referred as “ET”) perform relevant EM&A programme and as well as the associated duties.
- 1.1.4 As part of the EM&A programme, Baseline Monitoring Report which determined Action and Limit Levels (A/L Levels) based on the baseline data, has been verified by Independent Environmental Checker (IEC) and submitted to EPD endorsement on **24 November 2021**. Also, construction activities of the Contract were commencement on **7 December 2021**.
- 1.1.5 This is **3rd** monthly EM&A report to presenting the monitoring results and inspection findings from **1** to **28 February 2022** of the Reporting Period.

1.2 REPORT STRUCTURE

- 1.2.1 The report was structured into the following sections:-

Section 1	<i>Introduction</i>
Section 2	<i>Project Organization and Construction Progress</i>
Section 3	<i>Summary of Impact Monitoring Requirements</i>
Section 4	<i>Construction Noise Monitoring</i>
Section 5	<i>Ecology Waterbirds Monitoring</i>
Section 6	<i>Waste Management</i>
Section 7	<i>Site Inspections</i>
Section 8	<i>Environmental Complaints and Non-Compliance</i>
Section 9	<i>Implementation Status of Mitigation Measures</i>
Section 10	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS**2.1 PROJECT ORGANIZATION**

- 2.1.1 The project organization is shown in [Appendix B](#). The roles and responsibilities of the various parties involved in the EM&A process and the organizational structure of the organizations responsible for implementing the EM&A programme are outlined below.

Water Supplies Department (WSD)

- 2.1.2 WSD is the Project Proponent and the Permit Holder of the EP of the development of the Project and will assume overall responsibility for the project. An Independent Environmental Checker (IEC) shall be employed by WSD to audit the results of the EM&A works carried out by the ET.

Environmental Protection Department (EPD)

- 2.1.3 EPD is the statutory enforcement body for environmental protection matters in Hong Kong.

Engineer or Engineers Representative (ER)

- 2.1.4 The ER is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the ER with respect to EM&A are:

- Supervise the Contractor's activities and ensure that the requirements in the Contract Works Specific EM&A Manual are fully complied with;
- Inform the Contractor when action is required to reduce impacts in accordance with the Event and Action Plans;
- Employ an IEC to audit the results of the EM&A works carried out by the ET; and
- Comply with the agreed Event Contingency Plan in the event of any exceedance.

The Main Contractor

- 2.1.5 The Main Contractor is responsible perform construction works and for ensuring that the works are undertaken compliance with the specification and contract requirements. The duties and responsibilities of the Main Contractor with respect to EM&A are:

- Employ an Environmental Team (ET) to undertake monitoring, laboratory analysis and reporting of environmental monitoring and audit;
- Provide assistance to ET in carrying out monitoring and auditing;
- Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event and Action Plans;
- Implement measures to reduce impact where Action and Limit levels are exceeded; and
- Adhere to the agreed procedures for carrying out compliant investigation.

Environmental Team (ET)

- 2.1.6 The ET is responsible perform implementation EM&A programmes of the Contract Works as stipulated in the Updated EM&A Manual ensure the works are fully compliance with environmental regulations. The duties and responsibilities of the ET with respect to EM&A are:

- Set up all the required environmental monitoring stations;
- Monitor various environmental parameters as required in the EM&A Manual;
- Analyze the EM&A data and review the success of EM&A programme to cost effectively confirm the adequacy of mitigation measures implemented and the validity of the EIA predictions and to identify any adverse environmental impacts arising;
- Carry out site inspection to investigate and audit the Contractors' site practice, equipment and work methodologies with respect to pollution control and environmental mitigation, and take proactive actions to pre-empt problems;
- Audit and prepare audit reports on the environmental monitoring data and site environmental conditions;
- Report on the EM&A results to the IEC, Contractor, the ER and EPD or its delegated representative;
- Recommend suitable mitigation measures to the Contractor in the case of exceedance of

- Action and Limit levels in accordance with the Event and Action Plans;
- Undertake regular and ad-hoc on-site audits / inspections and report to the Contractor and the ER of any potential non-compliance; and
- Follow up and close out non-compliance actions.

Independent Environmental Checker (IEC)

2.1.7 The duties and responsibilities of IEC with respect to EM&A are:

- Review the EM&A works performed by the ET (at not less than monthly intervals);
- Audit the monitoring activities and results (at not less than monthly intervals);
- Report the audit results to the ER and EPD in parallel;
- Review the EM&A reports (monthly summary reports) submitted by the ET;
- Review the proposal on mitigation measures submitted by the Contractor in accordance with the Event and Action Plans;
- Check the mitigation measures submitted by the Contractor in accordance with the Event and Action Plans;
- Check the mitigation measures that have been recommended in the EIA and this Manual, and ensure they are properly implemented in a timely manner, when necessary;
- Report the findings of site inspections and other environmental performance reviews to ER and EPD;
- Coordinate the monitoring and auditing works for all the on-going contracts in the area in order to identify possible sources / causes of exceedances and recommend suitable remedial actions where appropriate; and
- Coordinate the assessment and response to complaints / enquires from locals, green groups, district councils or the public at large.

2.2 CONSTRUCTION PROGRESS

2.2.1 In the Reporting Period, major construction activities of the Contract Works are listed in below. Moreover, a master construction program is enclosed in [Appendix C](#).

- Site formation works
- Piling Work

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 To according with the EP stipulation, the required documents has submitted to EPD for retention as listed below:

- Project Location Plans;
- Updated Environmental Monitoring and Audit Manual of Project Specific (TCS01176/21/600/R0012v2); and
- Baseline Monitoring Report (TCS01216/21/600/R0017v3) for the Project.

2.3.2 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project is presented in **Table 2-3-1**.

Table 2-3-1 Status of Environmental Licenses and Permits

Item	Description	Licence/Permit Status		
		Ref. no.	Effective Date	Expiry Date
1	Air Pollution Control (Construction Dust) Regulation	Notification was made on 3 Aug 2021	3 Aug 2021	Till the Contract ends
2	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account No.: 7041397	8 Aug 2021	Till the Contract ends
3	Chemical Waste Producer Registration	Application was made on 3 Aug 2021	3 Aug 2021	Till the Contract ends
4	Water Pollution Control Ordinance – Discharge Licence	Discharge Licence No.: WT00039707-2021	17 Nov 2021	30/11/2026
5	Construction Noise Permit	CNP No. GW-RN0857-21	24 Nov 2021	23 Feb 2022

3. SUMMARY OF IMPACT MONITORING REQUIREMENTS**3.1 GENERAL**

- 3.1.1 According to the Updated EM&A Manual and the location of the Contract Works, only construction noise monitoring and waterbirds ecological of environmental monitoring are related the Contract Works during the construction phase. Details requirement of noise and waterbirds ecological impact monitoring are presented sub-sections as below.

3.2 REQUIREMENT OF CONSTRUCTION NOISE MONITORING

- 3.2.1 One set of $L_{eq(30min)}$ as 6 consecutive $L_{eq(5min)}$ between 0700-1900 hours on normal weekdays and once every week during course of works. If construction work necessary to carry out at other time periods, i.e. restricted time period (19:00 to 07:00 the next morning and whole day on public holidays) (hereinafter referred as “the restricted hours”), $L_{eq(5min)}$ measurement will be carried out in accordance with the CNP requirements. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

- 3.2.2 Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.3 LOCATION OF CONSTRUCTION NOISE IMPACT MONITORING

- 3.3.1 According to the Updated EM&A Manual of CEDD Contract No. NDO 14/2018 - *Advance and First Stage Works of Kwu Tung North and Fanling North New Development Areas*, four noise sensitive receivers are designated on Fanling North New Development Areas for construction noise monitoring.

- 3.3.2 According to the geographic location of proposed Shek Wu Hui Water Reclamation Plant and all the recommended designated construction noise monitoring stations, only the designated noise monitoring station CP-KTN-NMS5 (prior named “CP-NMS7”) shown in [Appendix D](#), is located near the proposed Shek Wu Hui Water Reclamation Plant within 300m (distance about 110m). Therefore, the designated noise monitoring station CP-KTN-NMS5 is recommended for the Contract Works to undertake construction noise monitoring. If the recommended noise monitoring location CP-KTN-NMS5 not available, the ET shall propose alternative monitoring locations/additional monitoring locations and seek approval from the Supervisor of the proposal. When alternative/new monitoring location is proposed, the monitoring location shall be chosen based on the following criteria:

- (i) at locations close to the major site activities which are likely to have noise impacts;
- (ii) close to the noise sensitive receivers; and
- (iii) for monitoring locations located in the vicinity of the sensitive receivers, care shall be taken to cause minimal disturbance to the occupants during monitoring.

- 3.3.3 The construction noise monitoring station shall normally be at a point 1 m from the exterior of the sensitive receivers building façade and be a position 1.2m above the ground. If there is problem with access to the normal monitoring position, an alternative position may be chosen, and a correction to the measurements shall be made to the free field measurements. The ET shall agree with the Supervisor on the monitoring station that is chosen for impact monitoring.

3.4 ACTION AND LIMIT LEVEL FOR CONSTRUCTION NOISE

- 3.4.1 The Action and Limit levels for construction noise are defined in **Table 3-4-1**. Should non-compliance of the criteria occur, action in accordance with the Action Plan which shown in Section 4 of this report, shall be carried out.

Table 3-4-1 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
CP-KTN-NMS5	When one or more documented complaints are received	75 dB(A) ^{Note 1}

Note 1: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the NCA have to be followed.

3.5 NOISE MONITORING METHODOLOGY

Monitoring Equipment

- 3.5.1 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications was used for carrying out the noise monitoring. Noise equipment used for impact monitoring is listed in **Table 3-5-1**.

Table 3-5-1 Equipment of Noise Impact Monitoring

Equipment	Model
Integrating Sound Level Meter	Rion NL – 52
Calibrator	B&K 4231

Remark: Sound level meter IEC 60651:1979 (Type 1) was replaced by 60672 (Type 1) in 2002 (Ref: <https://webstore.iec.ch/publication/17086>)

- 3.5.2 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis. The valid calibration certificates of the monitoring equipment are shown in **Appendix E**.

3.6 MONITORING PROCEDURE

- 3.6.1 All noise measurements were performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq_(30min) in six consecutive Leq_(5min) measurements was used as the monitoring parameter for the time period between 07:00-19:00 hours during the baseline monitoring.
- 3.6.2 In general, the sound level meter would be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone was pointed to the site with the microphone facing perpendicular to the line of sight. The windshield would be fitted for all measurement. Where a measurement was to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement was to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.
- 3.6.3 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements would be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 3.6.4 Noise measurements would not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed would be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.7.1 The monitoring data recorded in the equipment would be downloaded directly from the equipment at each monitoring day. The downloaded monitoring data would input into a computerized database properly maintained and handled by the ET's in-house data recording and management system.

3.8 REQUIREMENT OF WATERBIRDS ECOLOGICAL IMPACT MONITORING

3.8.1 Where development under the NDAs project is undertaken within 200m (the maximum distance at which it is predicted there may be some disturbance, and hence a reduction in numbers, of large waterbirds) of the Ng Tung, Sheung Yue and Shek Sheung Rivers and Long Valley the monitoring protocol detailed in the updated EM&A Manual Table 12.1 should be followed. A transect should be undertaken throughout the sections of the rivers where NDA construction activities are proposed; as the sensitive receivers (large waterbirds) are easily visible, the transect route needs only follow one bank of the rivers. The transect route should remain the same during the different phases in order to ensure that data are comparable. Monitoring of large waterbirds should be conducted in pre-construction, construction and operational phases of the concerned development.

3.8.2 The proposed Shek Wu Hui Water Reclamation Plant location is located less than 200m to Ng Tung River, Sheung Yue River and Shek Sheung River, waterbirds ecological monitoring included pre-construction (i.e. baseline), construction (i.e. impact) and post-construction (i.e. operating) should be requires. The detailed monitoring protocol is listed in *Table 3-8-1*.

Table 3-8-1 Monitoring of Measures to Minimize Disturbance to Waterbirds on the Ng Tung, Sheung Yue and Shek Sheung Rivers

Phase	Methodology
Pre-construction (baseline)	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels for 12 months prior to the commencement of construction.
Construction	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to construction activities throughout the construction period.
Post-construction	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to operational activities for 12 months following the completion of the construction period.

3.8.3 Waterbirds ecological baseline monitoring at Ng Tung River, Sheung Yue River and Shek Sheung River was conducted by DSD between *December 2017* and *June 2019* (total 19 months baseline monitoring), in compliance with the Updated EM&A Manual. Thus, the action and limit levels and responses to evidence of disturbance to waterbirds using in Ng Tung, Sheung Yue and Shek Sheung Rivers will be made reference during construction phase of the Project.

3.9 MONITORING METHODOLOGY FOR WATERBIRDS ECOLOGICAL IMPACT MONITORING

3.9.1 Three transects and seven point count locations were selected at the Ng Tung, Sheung Yue and Shek Sheung River. These locations are shown in Appendix K and summarized in *Table 3-9-1*.

Table 3-9-1 Ecological Monitoring Stations

Monitoring Stations	Descriptions	Influenced by Tidal Action
Transect T1	Along Ng Tung River	No
Transect T2		
Point Count Location P1		
Point Count Location P2		
Point Count Location P3		
Point Count Location P4		
Point Count Location P5	At Shek Sheung River (Low-flow Channel)	No
Transect T3	Along Shek Sheung River & Sheung Yue River	Yes
Point Count Location P6	At Shek Sheung River	Yes
Point Count Location P7	At Intersection between Sheung Yue and Shek Sheung River	Yes

- 3.9.2 Surveys will be conducted on a weekly basis at both high and low tides (it is considered high tide when tidal levels are above 1.5m and low tide when tidal level are below 1.5m at Tsim Bei Tsui Station).
- 3.9.3 All avifauna species that were seen or heard would be identified and quantified along transects and at point count locations. Survey data would be recorded continuously by the surveyor as they walk along the transects, while survey data of each point count location would be collected for 5-minutes after surveyor reaches the designated point count location.
- 3.9.4 Noticeable behaviours such as breeding, nesting, roosting, feeding and presences of recently fledged juveniles were recorded and reported. In the case which such behaviours were observed for species of conservation importance, the Resident Engineer (RE), the Contractor and the Independent Environmental Checker (IEC) would be immediately notified after the survey such that the Contractor could review the current construction programme and minimize disturbances due to construction activities.

3.10 EVENT ACTION PLAN

Noise

- 3.10.1 Should non-compliance of the construction noise criteria occur, action in accordance with the Action Plan in **Table 3-10-1** shall be carried out.

Table 3-10-1 Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	1. Notify the IEC, ER and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the monitoring data submitted by the ET; 2. Review the construction methods and proposed remedial measures by the Contractor, and advise the ET and ER if the proposed remedial measures would be sufficient; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify the Contractor; 3. Require the Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals to the ER and IEC and copy to the ET; 2. Implement noise mitigation proposals.
Limit Level Exceedance	1. Identify sources. 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase the monitoring frequency; 5. Carry out analysis of the Contractor's working procedures with the ER and Contractor to determine possible mitigations to be implemented; 6. Inform IEC, ER, EPD and Contractor the causes and	1. Discuss amongst the ER, ET and Contractor on the potential remedial actions; 2. Review the Contractor's remedial action whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing; 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analyzed noise problems; 4. Ensure remedial measures are properly implemented; 5. If exceedance continues,	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial action to the ER and IEC and copy to the ET within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit

Event	Action			
	ET	IEC	ER	Contractor
	actions taken for the exceedances; 7. Assess the effectiveness of the Contractor's remedial action with the ER and keep the IEC informed of the results; 8. If exceedance stops, cease additional monitoring.		consider what portion of work is responsible and instruct the Contractor to stop that portion of works until the exceedance is abated.	proposals if problems still not under control; stop the relevant portion of works as determined by the ER until the exceedance is abated.

Waterbird of Ecological

- 3.10.2 Should any exceedance encountered during construction phase, action in accordance with the Action Plan listed in **Table 3-10-2** shall be carried out.

Table 3-10-2 Event and Action Plan of Waterbirds of Ecological

Action Level	Response	Limit Level	Response
Construction Phase			
Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Action Level response is triggered.	Investigate cause and if cause identified as related to NDAs project instigate remedial action to remove or reduce source of disturbance.	Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Limit Level response is triggered.	Investigate cause and if caused identified as related to NDAs project instigate remedial action. Review and adjust LVNP management measures to improve conditions for affected species.
Decline in numbers of any one waterbird species occurring in significant numbers* during Baseline Monitoring such that the Action Level response is triggered.	Investigate cause and if cause identified as related to NDAs project instigate remedial action to remove or reduce source of disturbance.	Decline in numbers of any one waterbird species occurring in significant numbers* during Baseline Monitoring such that the Limit Level response is triggered.	Investigate cause and if caused identified as related to NDAs project instigate remedial action. Review and adjust LVNP management measures to improve conditions for affected species.

(*) *Waterbird numbers refer to combined numbers using the channels*

4. CONSTRUCTION NOISE MONITORING**4.1 GENERAL**

- 4.1.1 The noise monitoring schedule is presented in [Appendix F](#) and the monitoring results are presented in the following sections.

4.2 RESULTS OF NOISE MONITORING

- 4.2.1 In the Reporting Period, a total of **4** occasions noise monitoring were carried out at the designated location CP-KTN-NMS5. The sound level meter was set in free-field situation, and therefore, façade correction (+3dB) is added according to acoustical principles and EPD guidelines. The noise monitoring results at the designated locations are summarized in **Tables 4-2-1**. The detailed noise monitoring data is presented in [Appendix G](#) and the relevant graphical plot shown in [Appendix H](#).

Table 4-2-1 Summaries of Noise Monitoring Results of CP-KTN-NMS5

Date	Start Time	L _{Aeq30min} (dB(A))
4-Feb-22	9:17	64
11-Feb-22	9:03	62
18-Feb-22	9:31	63
23-Feb-22	9:57	60
Limit Level		75 dB(A)

Note: façade correction +3dB has added according to acoustical principles and EPD guidelines

- 4.2.2 During construction noise monitoring, no rain was encountered and wind speed is below 5m/s and gusts not exceeding 10m/s.
- 4.2.3 As shown in **Table 4-2-1**, the noise level measured at the designated monitoring location was below 75dB(A). Furthermore, there were no noise complaints (Action Level exceedance) received by the RE, Contractor, WSD or EPD in the Reporting Period. Therefore, no Action or Limit Level exceedance was triggered and no corrective action was therefore required.
- 4.2.4 During the reporting period, no construction work was carried out during restricted hours.

5. ECOLOGY WATERBIRD MONITORING**5.1 GENERAL**

- 5.1.1 Ecological monitoring for waterbirds shall be performed as transects and point count surveys along Ng Tung River, Sheung Yue River and Shek Sheung River in accordance with general surveying practices.
- 5.1.2 The surveying shall be undertaken by a qualified ecologist and he/she shall be a member of the ET. Throughout the construction period, weekly transect shall be conducted at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to construction activities.
- 5.1.3 Since occurrence of waterbirds has distinctive seasonal pattern, the construction phase data for all waterbirds and representative waterbirds shall be compared with the baseline data for the respective month and season. Total number of Waterbirds and six representative Waterbird species are used as an indicator of the level disturbance to water birds at each of the survey location. The representatives of waterbirds are listed in *Table 5-1-1*.

Table 5-1-1 Representative Waterbirds

Species Name	Common Name	Chinese Name
<i>Egretta garzetta</i>	Little Egret	小白鷺
<i>Ardea alba</i>	Great Egret	大白鷺
<i>Ardea cinerea</i>	Grey Heron	蒼鷺
<i>Ardeola bacchus</i>	Chinese Pond Heron	池鷺
<i>Bubulcus coromandus</i>	Eastern Cattle Egret	牛背鷺
<i>Phalacrocorax carbo</i>	Great Cormorant	普通鸕鶿

5.2 RESULTS OF WATERBIRDS SURVEY

- 5.2.1 Four (4) occasion of waterbirds survey were conducted in the Reporting Month.
- 5.2.2 Abundance and diversity of key waterbirds species in the Reporting Month are summarized in **Table 5-2-1** and **Table 5-2-2**.

Table 5-2-1 Total Bird Species and Abundance in the Reporting Month

Category	Number of Species	Abundance
All Avifauna	49	402
Waterbirds	16	151

Table 5-2-2 Total Bird Species and Abundance in the Reporting Month

Common Name	Species Name	Chinese Name	Abundance
Chinese Pond Heron	<i>Ardeola bacchus</i>	池鷺	11
Eastern Cattle Egret	<i>Bubulcus coromandus</i>	牛背鷺	11
Grey Heron	<i>Ardea cinerea</i>	蒼鷺	23
Great Egret	<i>Ardea alba</i>	大白鷺	32
Little Egret	<i>Egretta garzetta</i>	小白鷺	38
Great Cormorant	<i>Phalacrocorax carbo</i>	普通鸕鶿	11

- 5.2.3 The result was compared with the baseline data. While the numbers of Eastern Cattle Egret, Great Egret and Little Egret are all on a similar level compared to the baseline data; the number of waterbirds as a whole, Chinese Pond Heron, Grey Heron, Little Egret and Great Cormorant were declined.
- 5.2.4 A table showing the waterbirds abundance comparison with baseline data was provided in **Appendix K**. (Appendix C of the waterbirds survey report).

- 5.2.5 A number of immediate sources of disturbances such as the fishing activities at all transect, discharge of sewage water at P3 and construction activities disturbance from different parties were identified by the surveyor during the monitoring events. Although noise from construction sites of different parties was reported by the surveyor, the measured noise monitoring result at the impact monitoring location CP-KTN-NMS5 of the Contract was at acceptable level.
- 5.2.6 In addition, it is suggested that the enhanced habitat of Long Valley Nature Park (LVNP) might also have caused a difference in composition and abundance of species that visit its nearby areas.
- 5.2.7 A clearer cause for the reduction in waterbird abundance could not be identified, but it could be theorized that the cumulative impacts of human disturbances and change in the surrounding habitats (including enhanced habitat of LVNP) are related to the decrease in waterbirds.
- 5.2.8 Since the measured noise levels recorded at the noise monitoring location CP-KTN-NMS5 in the Reporting Month were at acceptable level and there are other factors that might cause the decrease in waterbirds, the cause of abundance decline was considered unlikely due to the Project. No action and limit level exceedance was considered triggered in the Reporting Month.
- 5.2.9 The details of the waterbirds survey for the Reporting Month can be referred to the full waterbirds survey report provided in **Appendix K**.

6. WASTE MANAGEMENT**6.1 GENERAL WASTE MANAGEMENT**

- 6.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

6.2 RECORDS OF WASTE QUANTITIES

- 6.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

- 6.2.2 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 6-2-1* and *6-2-2* and the Monthly Summary Waste Flow Table is shown in *Appendix I*. Whenever possible, materials were reused on-site as far as practicable.

Table 6-2-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) (in '000m ³)	0.5411	-
Reused in this Contract (Inert) (in '000 m ³)	0	-
Reused in other Contracts/ Projects (Inert) (in '000 m ³)	0	-
Disposal as Public Fill (Inert) (in '000 m ³)	0.5411	TM38

Table 6-2-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity	Disposal Location
Recycled Metal ('000kg)	0	-
Recycled Paper / Cardboard Packing ('000kg)	0	-
Recycled Plastic ('000kg)	0	-
Chemical Wastes ('000kg)	0	-
General Refuses ('000m ³)	0.0019	SENT

7. SITE INSPECTION

7.1 REQUIREMENTS

- 7.1.1 According to the approved Updated EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

- 7.2.1 In the Reporting Month, weekly regular site inspection by the RE, the Main Contractor and ET was carried out on **4, 10, 18 and 23 February 2022** to evaluate site environmental performance of the Contract Works. During the four occasion site inspections, no non-compliance was noted.

- 7.2.2 The findings/deficiencies of the Contract Works observed that during the weekly site inspection are listed in **Table 7-2-1**.

Table 7-2-1 Site Observations

Date	Findings / Deficiencies	Follow-Up Status
4 Feb 2022	<ul style="list-style-type: none"> Cement bags on the ground was observed. The Contractor was advised to cover it with tarpaulin sheets properly. 	Cement bags were covered properly with tarpaulin sheet.
10 Feb 2022	<ul style="list-style-type: none"> Chemical containers should be placed inside drip tray to avoid land contamination Opened cement bags was observed. The Contractor should treat them properly to avoid dust generation. NRMM label for the crawler crane should be renewed. General refuse stored on site should be cleaned regularly. 	<p>Chemical containers were removed from site.</p> <p>Open cement bags were removed from site.</p> <p>NRMM label was renewed.</p> <p>General refuse was removed regularly</p>
18 Feb 2022	<ul style="list-style-type: none"> Chemical container should be placed inside drip tray to avoid any land contamination. Stockpile should be properly covered to reduce dust generation. 	<p>Chemical containers were removed from site.</p> <p>Stockpile was covered with tarpaulin sheet.</p>
23 Feb 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed during site inspection. 	NA

8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION**

- 8.1.1 For the Contract Works, no environmental complaint, summons and prosecution was received in the Reporting Period. The statistical summary table of environmental complaint is presented in *Tables 8-1-1, 8-1-2 and 8-1-3*.

Table 8-1-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

Table 8-1-2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

Table 8-1-3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 28 February 2022	0	0	NA

9. IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.1 GENERAL REQUIREMENTS

9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved Updated EM&A Manual covered the issues of dust, noise, water, ecological and waste and they are summarized presented in [Appendix J](#).

9.1.2 The Contract Works shall be implementing the required environmental mitigation measures according to the approved Updated EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented by the Main Contractor in this Reporting Month are summarized in **Table 9-1-1**.

Table 9-1-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> Wastewater to be treated by filtration system such as sedimentation tank and storage on-site. After Wastewater Discharge Permit is obtained to carry out dispose.
Air Quality	<ul style="list-style-type: none"> Maintain damp / wet surface on access road Keep slow speed in the sites All vehicles must use wheel washing facility before off site Sprayed water during breaking or excavation works Soil stockpile greater than 50m³ has cover with plastic sheets
Noise	<ul style="list-style-type: none"> Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants Shut down the plants when not in used.
Waste and Chemical Management	<ul style="list-style-type: none"> Follow requirements and procedures of the “Trip-ticket System” The site was generally kept tidy and clean.

9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

9.2.1 The construction works under the Contract Works in the coming month are listed below:

- Site formation works
- Piling Work

9.3 KEY ISSUES FOR THE COMING MONTH

9.3.1 Key issues to be considered in the coming month for the Contract Works include:

- Implementation of control measures for rainstorm;
- Regular clearance of stagnant water during wet season;
- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

9.3.2 The Main contractor should pay special attention on noise and dust and water quality mitigation measures and fully implement according to the ISEMM of the approved Updated EM&A Manual.

10. CONCLUSIONS AND RECOMMENDATIONS**10.1 CONCLUSIONS**


- 10.1.1 This is **3rd** monthly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from **1** to **28 February 2022**.
- 10.1.2 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in the Reporting Period. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 Four (4) occasions of the weekly waterbirds survey has been taken in the Reporting Period. Although decrease in waterbirds abundance was recorded in the Reporting Period, the cause of abundance decline was considered unlikely due to the Project. No action and limit level exceedance was considered triggered in the Reporting Month.
- 10.1.4 No documented complaint, notification of summons or successful prosecution was received by either the RE or CEDD or the Main Contractor.
- 10.1.5 Weekly site inspection by the RE, ET and the Main Contractor had carried out on **4, 10, 18** and **23 February 2022**. The mitigation measures implemented was considered satisfactory. No non-compliance observed during the site inspection.

10.2 RECOMMENDATIONS

- 10.2.1 During dry season and in consideration of construction site under the Contract Works is located adjacent to villages, the Main Contractor should fully implement air quality mitigation measures to reduce construction dust emission.
- 10.2.2 Construction noise would be a key environmental issue during construction work of the Contract Works. Noise mitigation measures such as using quiet plants should be implemented in accordance with the approved Updated EM&A Manual requirement.
- 10.2.3 In addition, all effluent discharge shall complied with discharge permits stipulation.
- 10.2.4 Moreover, mosquito control should be implemented to prevent mosquito breeding on site; and daily cleaning and weekly tidiness shall be properly performed.

Appendix A

Location of Shek Wu Hui Water Reclamation Plant

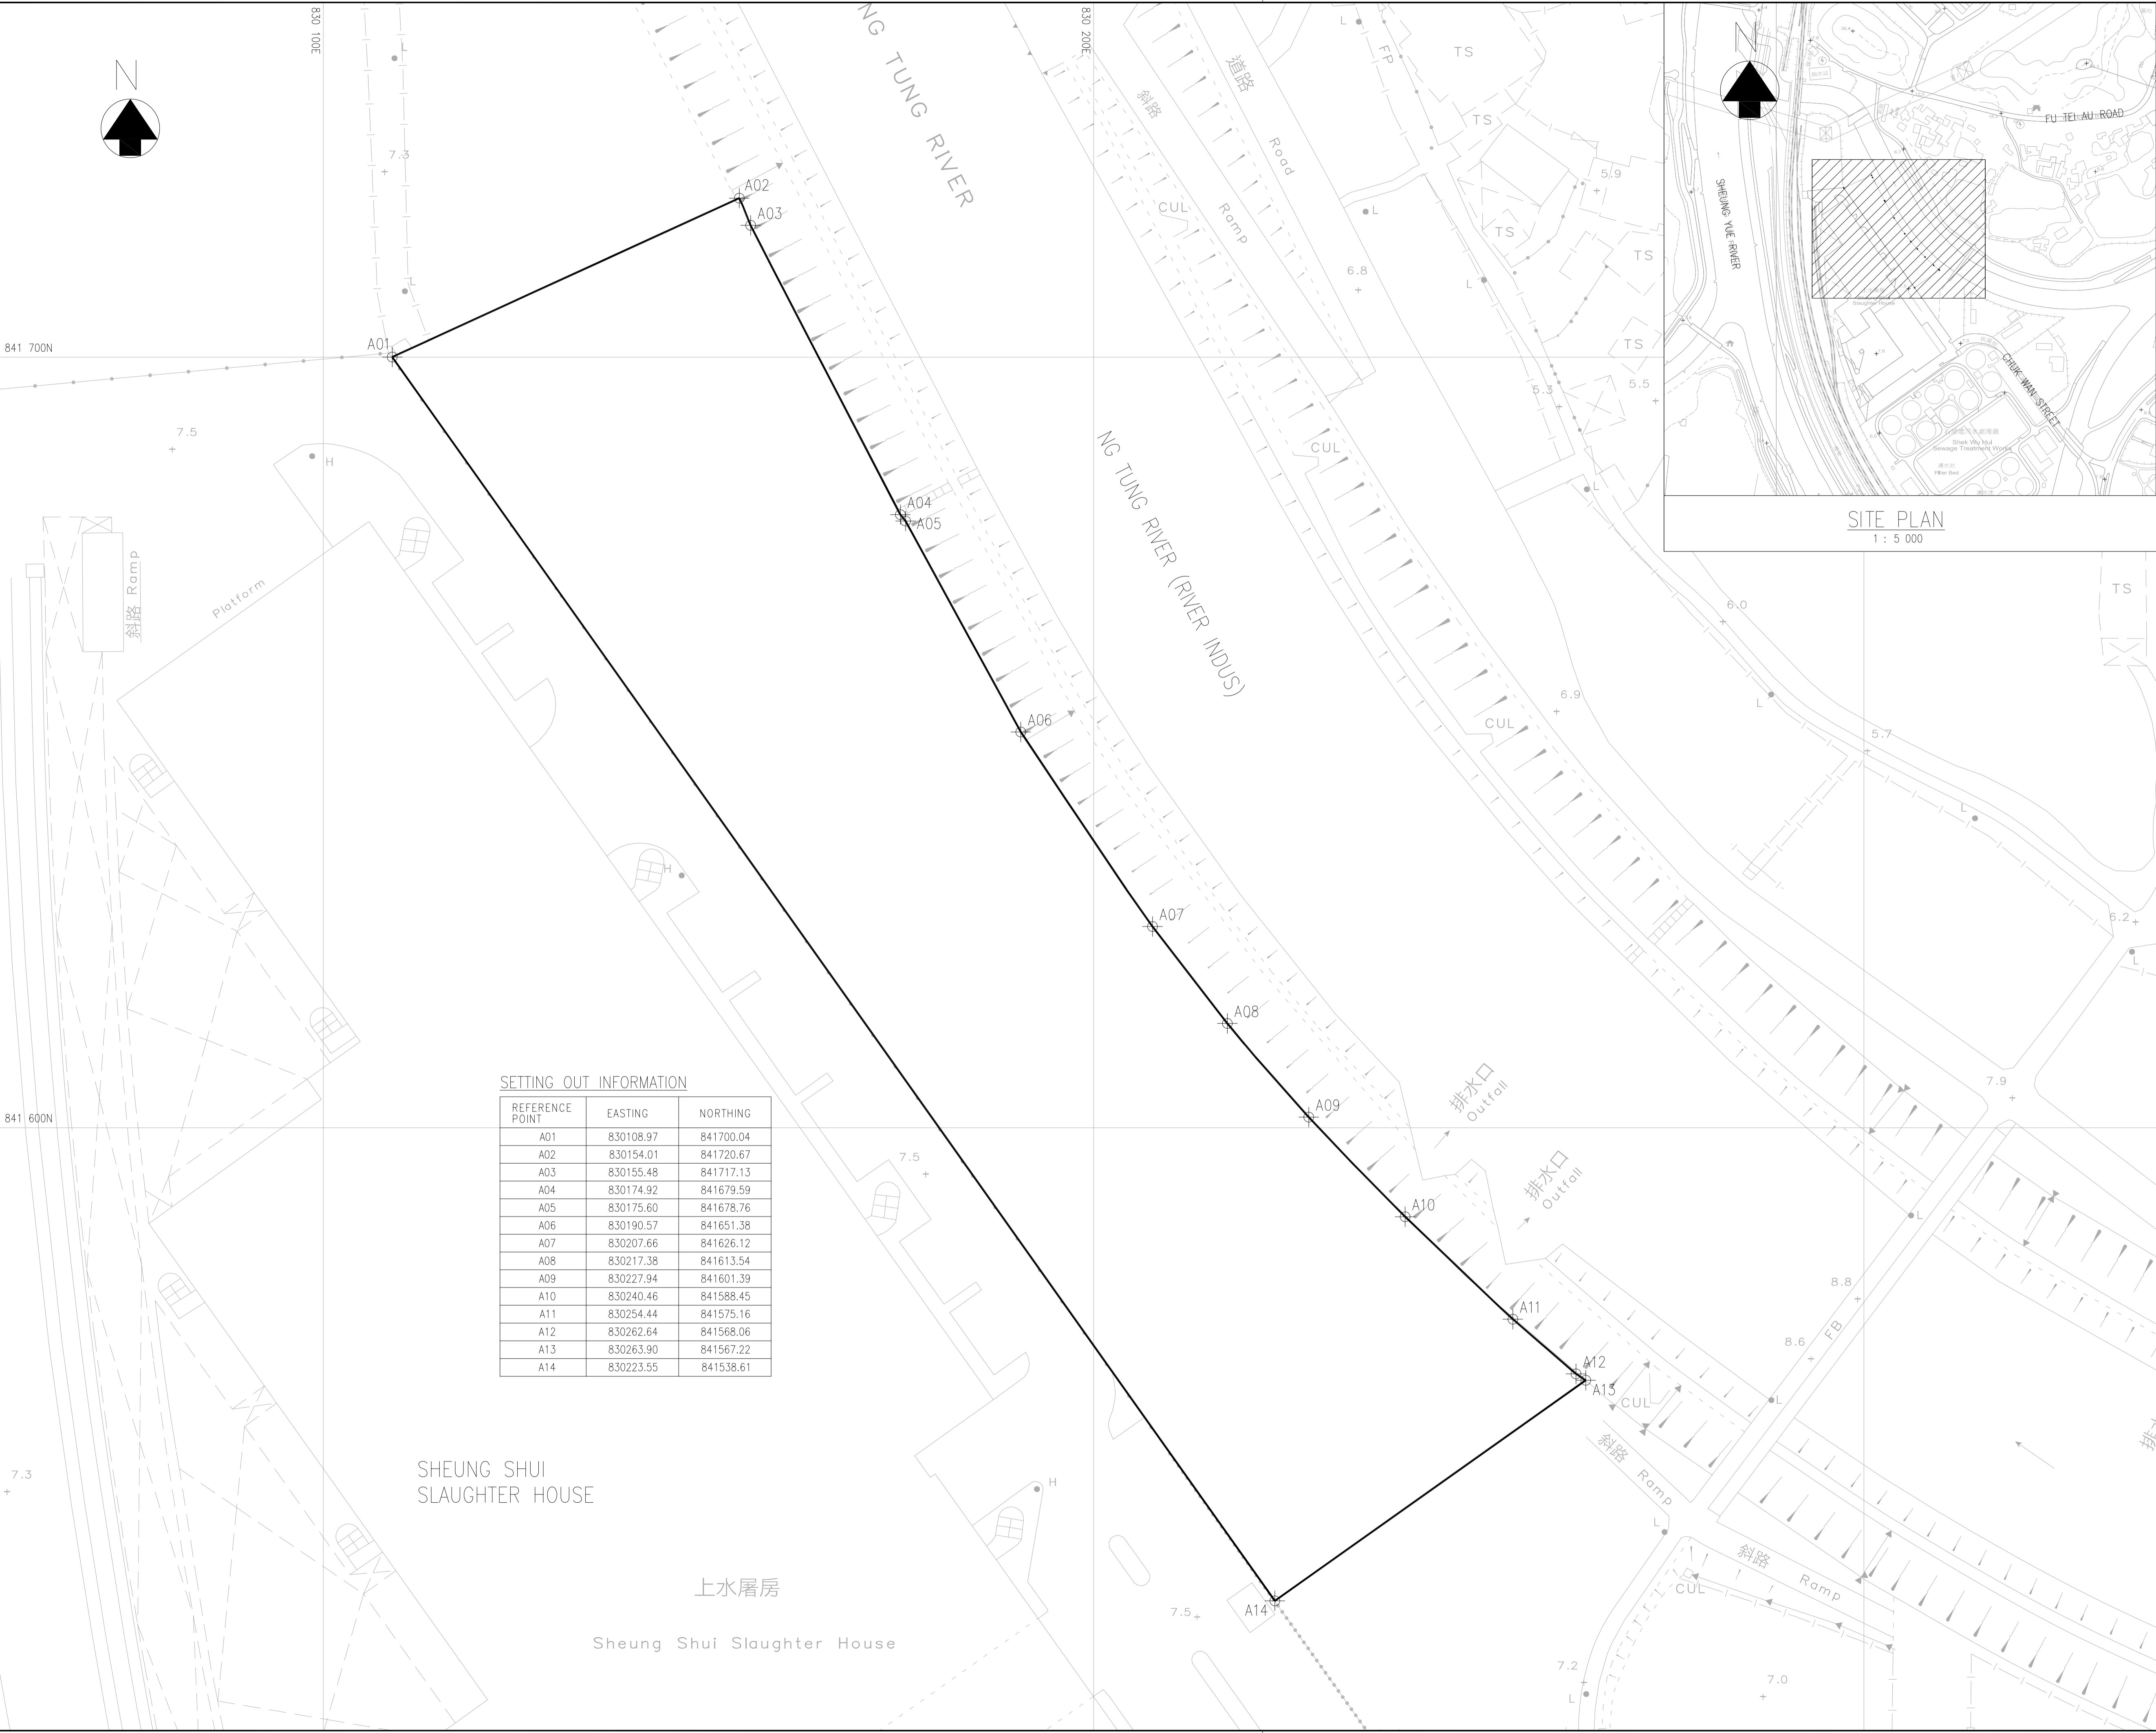


SETTING OUT INFORMATION

REFERENCE POINT	EASTING	NORTHING
A01	830108.97	841700.04
A02	830154.01	841720.67
A03	830155.48	841717.13
A04	830174.92	841679.59
A05	830175.60	841678.76
A06	830190.57	841651.38
A07	830207.66	841626.12
A08	830217.38	841613.54
A09	830227.94	841601.39
A10	830240.46	841588.45
A11	830254.44	841575.16
A12	830262.64	841568.06
A13	830263.90	841567.22
A14	830223.55	841538.61

SHEUNG SHUI
SLAUGHTER HOUSE

上水屠房

Sheung Shui Slaughter House

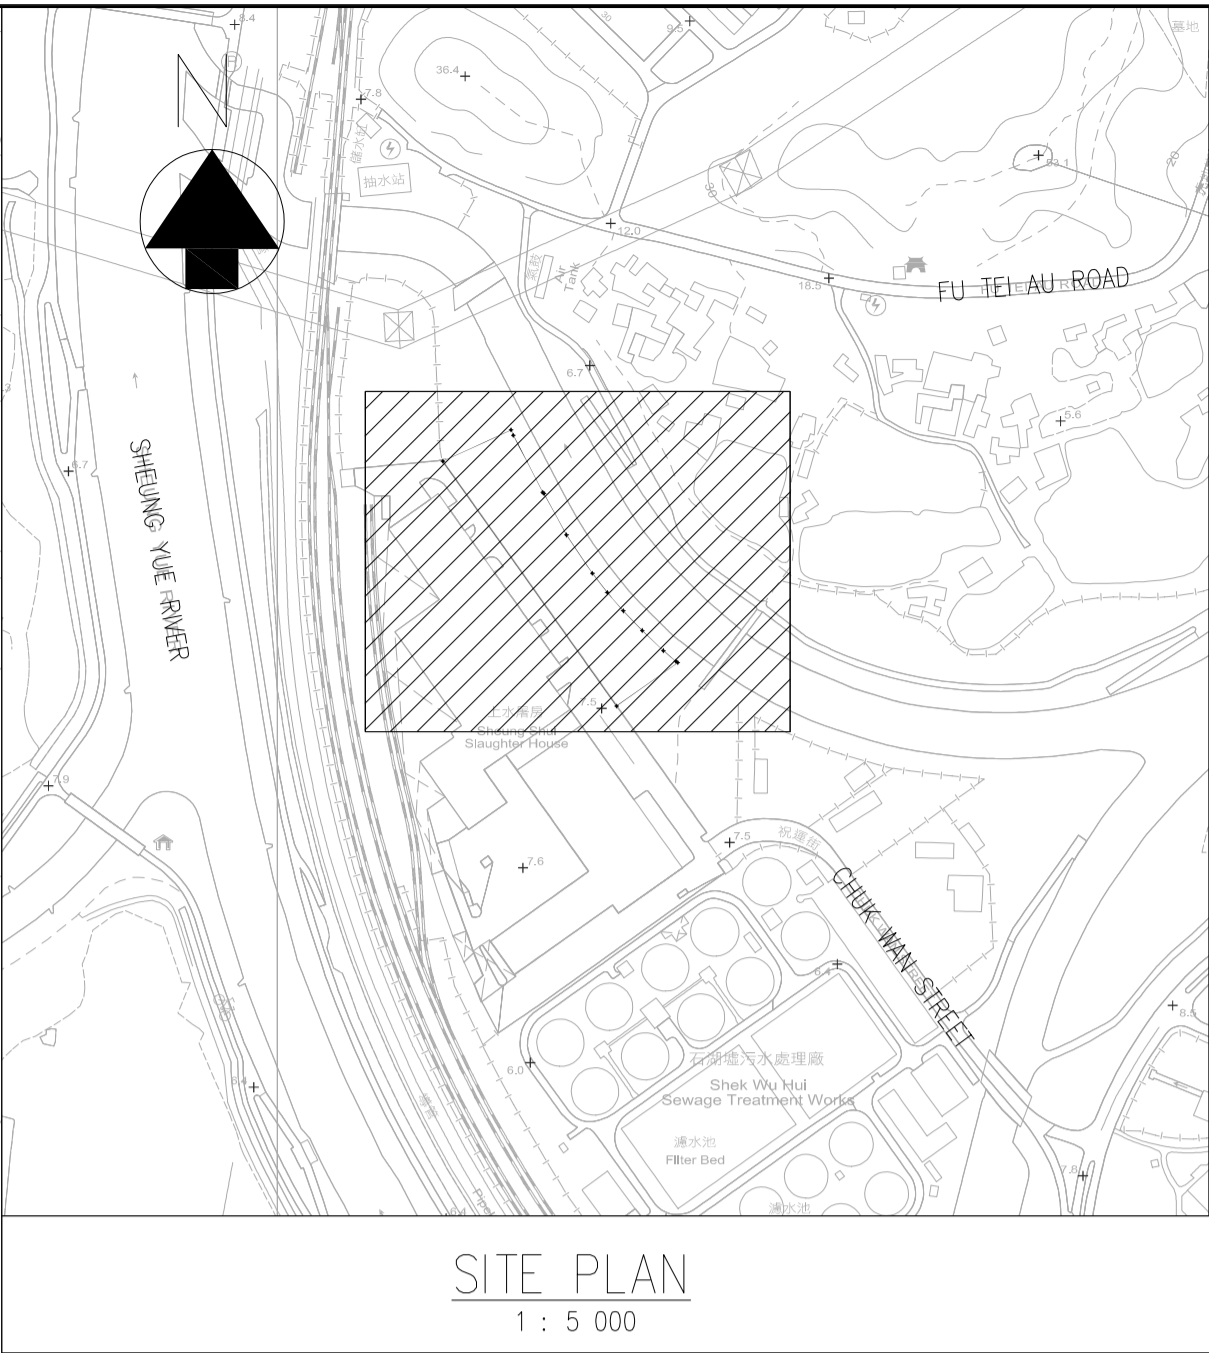

Copyright by Binnies Hong Kong Limited

NOTES:
COPYRIGHT RESERVED
THIS PRINT MAY NOT BE COPIED, TRACED, OR EXHIBITED WITHOUT PERMISSION OF THE WATER AUTHORITY.

- ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE SPECIFIED.
- THE BASE PLAN IS EXTRACTED FROM SURVEY SHEET NOS. 2-SE AND 3-SW.

Revision	Date	Description	Initial
Initial	Designed	Checked	Drawn
Initial	CWC	WH	SZ
Date	02/21	02/21	02/21

Approved

Contract No.

3/WSD/20

Contract Title

RECLAIMED WATER SUPPLY TO
SHEUNG SHUI AND FANLING

Drawing Title

SWHWRP
(PART 1 OF THE SITE) –
SETTING OUT PLAN

Drawing No.	Revision
401582/B&V/WRP/GN/201	–

Scale

A1 1 : 400
A3 1 : 800


水務署
Water Supplies
Department

BINNIES HONG KONG LIMITED
賓尼士工程顧問有限公司

Appendix B

Project Organization

Project Organization Chart

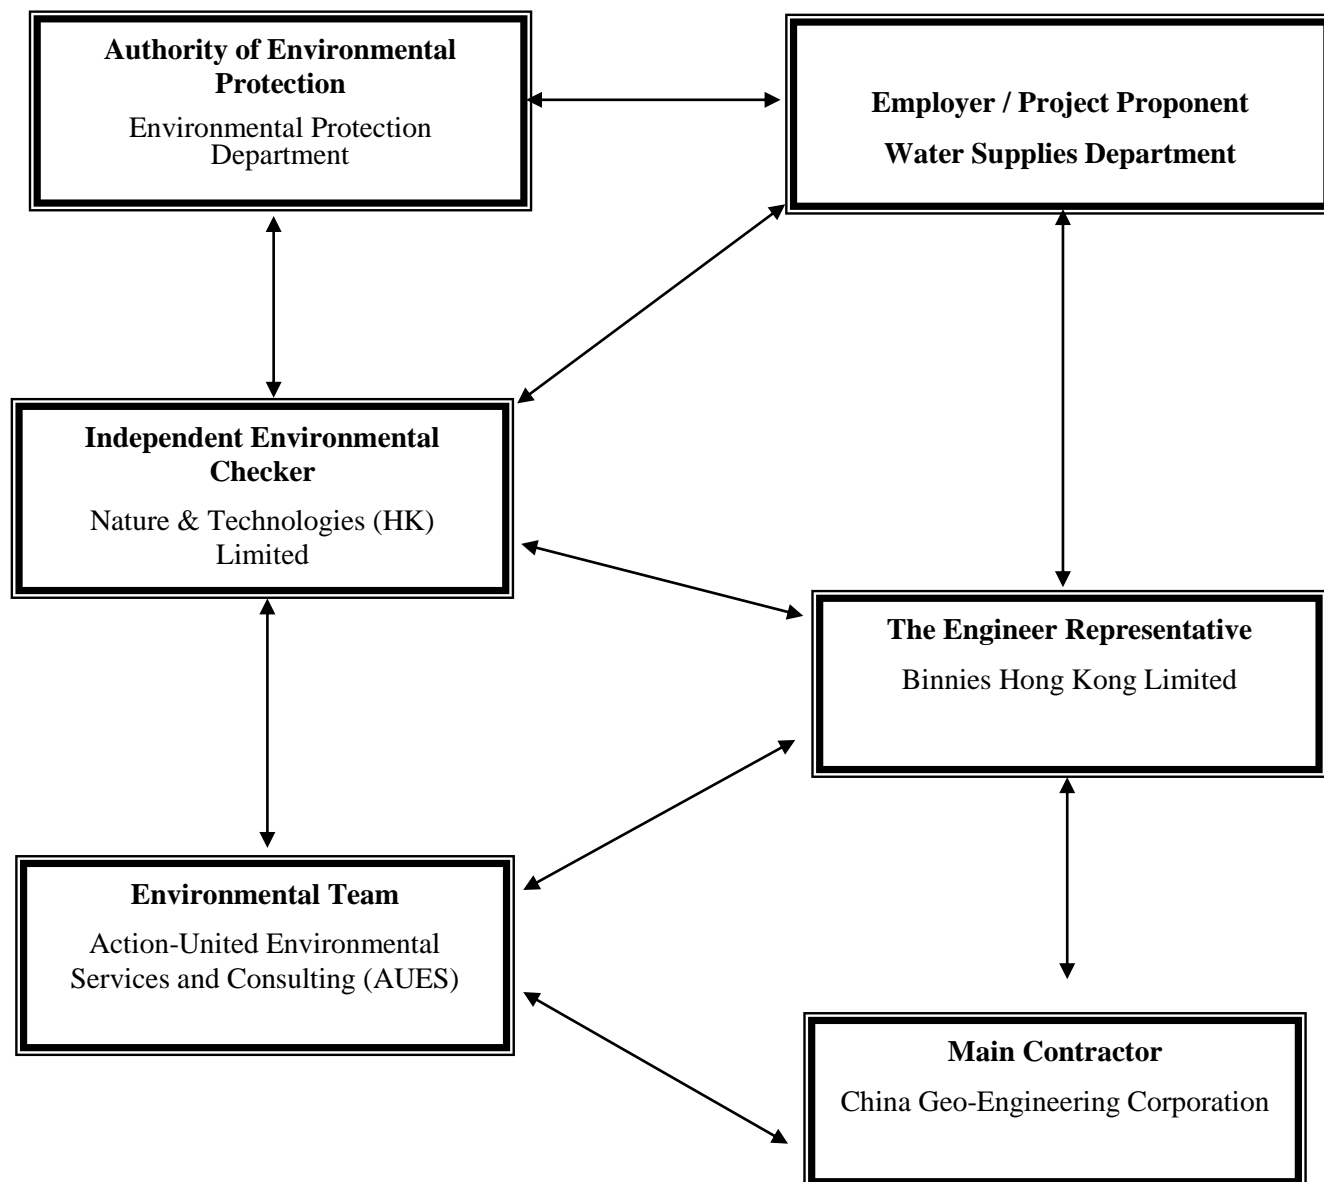

Contact Details of Key Personnel for the Project

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
WSD	Project Proponent	Tim Wong	2829 5638	2586 1696
Binnies	Senior Resident Engineer	S.H. Chung	2608 7380	TBC
Binnies	Resident Engineer	Chester Chan,	2608 7380	TBC
N&T	Independent Environmental Checker	Vega Wong	2877 3122	2511 0922
CGC	Site Agent	Kelvin Tsoi	5211 3332	TBC
CGC	Environmental Officer	Luke Chung	6488 0975	TBC
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Martin Li	2959 6059	2959 6079
AUES	Assistant Environmental Consultant	Fai So	2959 6059	2959 6079

Legend:*WSD (Employer) – Water Supplies Department**Binnies (Engineer Representative) – Binnies Hong Kong Limited**CGC (Main Contractor) – China Geo-Engineering Corporation**N&T (IEC) – Nature & Technologies (HK) Limited**AUES (ET) – Action-United Environmental Services and Consulting (AUES)*

Appendix C

Master Construction Program

ID	Task Name	Duration	Start	Finish	TRA	Notes	2022				2023				2024				2025				2026								
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3							
1	Contract Key Dates	1676 days	Jul 30 '21	Mar 1 '26																											
2	Contract Date	1 day	Jul 30 '21	Jul 30 '21																											
3	Starting Date	1 day	Jul 30 '21	Jul 30 '21																											
4	Contract Period	1675 days	Jul 31 '21	Mar 1 '26																											
5	Section 1 - Shek Wu Hui Water Reclamation Plant (SWHWRP)	791 days	Jul 31 '21	Sep 29 '23																											
6	Section 2 - Landscaping works of SWHWRP	791 days	Jul 31 '21	Sep 29 '23																											
7	Section 3 - Modification of Table Hill Reclaimed Water Service Reservoir	791 days	Jul 31 '21	Sep 29 '23																											
8	Section 4 - Mainlaying works in part 3 of the Site	791 days	Jul 31 '21	Sep 29 '23																											
9	Section 5 - Mainlaying works in part 4 of the Site	1095 days	Jul 31 '21	Jul 29 '24																											
10	Section 6 - Mainlaying works in part 5 of the Site	1279 days	Jul 31 '21	Jan 29 '25																											
11	Section 7 - Mainlaying works in part 6 of the Site	1522 days	Jul 31 '21	Sep 29 '25																											
12	Section 8 - Mainlaying works in part 7 of the Site & remaining WM works	1675 days	Jul 31 '21	Mar 1 '26																											
13	Section 9 - Conversion works of reclaimed water	1675 days	Jul 31 '21	Mar 1 '26																											
14	Contract Completion date	0 days	Mar 1 '26	Mar 1 '26																											
15																															
16	Preliminary & General	1062 days	Jul 30 '21	Jun 25 '24																											
17	Submission of Draft Safety Plan	14 days	Jul 30 '21	Aug 12 '21																											
18	Submission of Draft Environmental Management Plan	14 days	Jul 30 '21	Aug 12 '21																											
19	Submission of Sub-contractor Management Plan	14 days	Jul 30 '21	Aug 12 '21																											
20	Notification & request for UU record from utility undertakers	14 days	Jul 30 '21	Aug 12 '21																											
21	Submission and acceptance of selection procedure for supplier	29 days	Aug 3 '21	Aug 31 '21																											
22	Submission and acceptance of selection procedure for subcontractor	35 days	Aug 3 '21	Sep 6 '21																											
23	Agreement on preliminary office layout	35 days	Aug 12 '21	Sep 15 '21																											
24	Provision of Project Manager’s Accommodation	152 days	Sep 10 '21	Feb 8 '22																											
25	Submission and acceptance of subletting package	14 days	Sep 10 '21	Sep 23 '21																											
26	Selection of Subcontractor	18 days	Sep 24 '21	Oct 11 '21																											
27	Erection of Project Manager’s Accommodation	120 days	Oct 12 '21	Feb 8 '22																											
28	Selection of Traffic Consultant	1027 days	Sep 3 '21	Jun 25 '24																											
29	Submission and acceptance of subletting package	14 days	Sep 3 '21	Sep 16 '21																											
30	Selection of traffic consultant	13 days	Sep 17 '21	Sep 29 '21																											
31	XP application for different Sections	1000 days	Sep 30 '21	Jun 25 '24																											
32	TTA application for different Sections	1000 days	Sep 30 '21	Jun 25 '24																											
33	Selection of Concrete Supplier	29 days	Sep 6 '21	Oct 4 '21																											
34	Submission and acceptance of subletting package	9 days	Sep 6 '21	Sep 14 '21																											
35	Selection of concrete supplier	20 days	Sep 15 '21	Oct 4 '21																											
36	Selection of Subcontractor for Excavation and ELS Works at SWHWRP	42 days	Oct 7 '21	Nov 17 '21																											
37	Submission and acceptance of subletting package	21 days	Oct 7 '21	Oct 27 '21																											
38	Selection of subcontractor	21 days	Oct 28 '21	Nov 17 '21																											
39	Selection of Subcontractor for Structural Works	39 days	Dec 1 '21	Jan 8 '22																											
40	Submission and acceptance of subletting package	21 days	Dec 1 '21	Dec 21 '21																											
41	Selection of subcontractor	18 days	Dec 22 '21	Jan 8 '22																											
42	Selection of Subcontractor for Mainlaying Works	35 days	Dec 1 '21	Jan 4 '22																											
43	Submission and acceptance of subletting package - open trench	21 days	Dec 1 '21	Dec 21 '21																											
44	Selection of subcontractor - open trench	14 days	Dec 22 '21	Jan 4 '22																											
45	Submission and acceptance of subletting package - trenchless	21 days	Dec 1 '21	Dec 21 '21																											
46	Selection of subcontractor - trenchless	14 days	Dec 22 '21	Jan 4 '22																											
47																															
48	Section 1 & 2 - Construction of SWHWRP and Landscaping Works	764 days	Aug 27 '21	Sep 29 '23																											

Project: 3WSD20 Programme
Date: Nov 29 '21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 1

ID	Task Name	Duration	Start	Finish	TRA	Notes																								
							Q2	Q3	Q4	2022				2023				2024				2025				2026				
							Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3					
193	Site Acceptance Test of Equipment/Systems with SOR	14 days	Jul 14 '23	Jul 27 '23																										
194	Submission	14 days	Jun 23 '23	Jul 6 '23																										
195	Submission of Testing Procedures & Commissioning Plan	14 days	Jun 23 '23	Jul 6 '23																										
196	Submission of As Fitted Drawings	14 days	Jun 23 '23	Jul 6 '23																										
197	Submission of Manual	14 days	Jun 23 '23	Jul 6 '23																										
198	Submission of Training Material	14 days	Jun 23 '23	Jul 6 '23																										
199	System Commissioning Test	60 days	Jul 28 '23	Sep 25 '23																										
200	Planned completion for section 1	0 days	Sep 29 '23	Sep 29 '23																										
201	Planned completion for section 2	0 days	Sep 29 '23	Sep 29 '23																										
202																														
203	Section 3 - Modification of Table Hill Reclaimed Water Service Reservoir	721 days	Oct 1 '21	Sep 21 '23																										
204	Access Date (part 2 of the Site)	1 day	Oct 1 '21	Oct 1 '21																										
205	Initial survey and condition survey	60 days	Aug 28 '22	Oct 26 '22																										
206	Installation of supplementary dosing and dyeing system	240 days	Oct 27 '22	Jun 23 '23																										
207	T&C of E&M equipment	90 days	Jun 24 '23	Sep 21 '23																										
208	Planned completion for section 3	0 days	Sep 21 '23	Sep 21 '23																										
209																														
210	Section 4 - Water main laying works in part 3 of the Site	792 days	Jul 30 '21	Sep 29 '23																										
211	Access Date (part 3 of the Site)	1 day	Jul 30 '21	Jul 30 '21																										
212	Initial survey	90 days	Jul 31 '21	Oct 28 '21																										
213	1st TMLG meeting	1 day	Oct 13 '21	Oct 13 '21																										
214	Application and approval of TTA	111 days	Oct 14 '21	Feb 1 '22	14																									
215	Implementation of TTA by stages	605 days	Feb 2 '22	Sep 29 '23																										
216	Mainlaying by open trench method (RW03 & RW43)	605 days	Feb 2 '22	Sep 29 '23																										
217	RW03 : DN600 DI pipe - 1092m	538 days	Feb 7 '22	Jul 29 '23																										
218	Team A CH345-380(35m) Stage 3A	21 days	Feb 7 '22	Feb 27 '22																										
219	Team A CH380-415(35m) Stage 4A	21 days	Feb 28 '22	Mar 20 '22																										
220	Team A CH415-450(35m) with IT Chamber Stage 5A	22 days	Mar 21 '22	Apr 11 '22																										
221	Team A CH310-345(35m) Stage 2A	24 days	Apr 12 '22	May 5 '22																										
222	Team A CH275-310(35m) Stage 1A	22 days	May 6 '22	May 27 '22																										
223	Team A CH450-485(35m) Stage 6A	23 days	May 28 '22	Jun 19 '22																										
224	Team A CH485-520(35m) with Flow Meter Chamber Stage 7A	38 days	Jun 20 '22	Jul 27 '22																										
225	Team A CH520-555(35m) Stage 8A	21 days	Jul 28 '22	Aug 17 '22																										
226	Team A CH555-590(35m) Stage 9A	21 days	Aug 18 '22	Sep 7 '22																										
227	Team A Pressure test CH275-590	8 days	Sep 8 '22	Sep 15 '22																										
228	Team A CH590-620(30m) Stage 10A	24 days	Sep 16 '22	Oct 9 '22																										
229	Team A CH620-650(30m) Stage 11A	21 days	Oct 10 '22	Oct 30 '22																										
230	Team A CH650-680(30m) Stage 12A	21 days	Oct 31 '22	Nov 20 '22																										
231	Team A CH680-710(30m) Stage 13A	21 days	Nov 21 '22	Dec 11 '22																										
232	Team A CH710-740(30m) Stage 14A	24 days	Dec 12 '22	Jan 4 '23																										
233	Team A CH740-770(30m) with IT Chamber & washed out chamber Stage 15A	41 days	Jan 5 '23	Feb 14 '23																										
234	Team A CH770-800(30m) Stage 16A	21 days	Feb 15 '23	Mar 7 '23																										
235	Team A CH800-830(30m) Stage 17A	21 days	Mar 8 '23	Mar 28 '23																										
236	Team A CH830-860(30m) Stage 18A	26 days	Mar 29 '23	Apr 23 '23																										
237	Team A CH860-890(30m) Stage 19A	22 days	Apr 24 '23	May 15 '23																										
238	Team A Pressure test CH275-1092	18 days	May 16 '23	Jun 2 '23																										
239																														
240	Team B CH980-1010 (30m) Stage 4B	21 days	Feb 7 '22	Feb 27 '22																										

Project: 3WSD20 Programme

Date: Nov 29 '21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 5

ID	Task Name	Duration	Start	Finish	TRA	Notes	2022				2023				2024				2025				2026				
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3			
241	Team B CH1010-1040 (30m) Stage 5B	21 days	Feb 28 '22	Mar 20 '22																							
242	Team B CH1040-1070 (30m) Stage 6B	22 days	Mar 21 '22	Apr 11 '22																							
243	Team B CH950-980 (30m) Stage 3B	24 days	Apr 12 '22	May 5 '22																							
244	Team B CH920-950 (30m) Stage 2B	22 days	May 6 '22	May 27 '22																							
245	Team B CH890-920 (30m) Stage 1B	23 days	May 28 '22	Jun 19 '22																							
246	Team B CH1070-1092 (22m) Stage 7B	36 days	Jun 20 '22	Jul 25 '22																							
247																											
248	Team C CH0-100 (100m)Stage 1C	77 days	Apr 1 '23	Jun 16 '23																							
249	Team C CH100-150 (50m)Stage 2C	94 days	May 2 '22	Aug 3 '22																							
250	Team C CH150-200 (50m)Stage 3C	94 days	Aug 1 '22	Nov 2 '22																							
251	Team C CH200-275 (75m)Stage 4C	100 days	Nov 3 '22	Feb 10 '23																							
252																											
253	Estimate inclement weather	41 days	Jun 3 '23	Jul 13 '23																							
254	Overall pressure test	8 days	Jul 14 '23	Jul 21 '23																							
255	Pipe connection and completion	8 days	Jul 22 '23	Jul 29 '23																							
256																											
257	RW43 : DN150 DI pipe - 1144m	570 days	Feb 2 '22	Aug 25 '23																							
258	CH180 to CH610 (430m)	420 days	Feb 2 '22	Mar 28 '23	15	45d/50m																					
259	CH180 to CH000 (180m)	150 days	Mar 29 '23	Aug 25 '23		60d/60m+90d																					
260	CH610 to CH1144 (534m)	525 days	Feb 2 '22	Jul 11 '23	30	45d/50m																					
261	Testing of water main	21 days	Aug 26 '23	Sep 15 '23	14																						
262	Connection at RW43 - CH1144	14 days	Sep 16 '23	Sep 29 '23																							
263	Planned completion for section 4	0 days	Sep 29 '23	Sep 29 '23																							
264																											
265	Section 5 - Water main laying works in part 4 of the Site	1096 days	Jul 30 '21	Jul 29 '24																							
266	Access Date (part 4 of the Site)	1 day	Jul 30 '21	Jul 30 '21																							
267	Initial survey	90 days	Jul 31 '21	Oct 28 '21																							
268	Application and approval of TTA	116 days	Nov 1 '21	Feb 24 '22																							
269	Mainlaying by trenchless method (RW04)	479 days	Feb 25 '22	Jun 18 '23																							
270	DN450 DI pipe (6 locations , total length 237m)	479 days	Feb 25 '22	Jun 18 '23	60																						
271	Mainlaying by open trench method (RW04)	886 days	Feb 25 '22	Jul 29 '24																							
272	DN450 DI Pipe - 3332m	886 days	Feb 25 '22	Jul 29 '24	45																						
273	Planned completion for section 5	0 days	Jul 29 '24	Jul 29 '24																							
274																											
275	Section 6 - Water main laying works in part 5 of the Site	1280 days	Jul 30 '21	Jan 29 '25																							
276	Access Date (part 5 of the Site)	1 day	Jul 30 '21	Jul 30 '21																							
277	Initial survey	90 days	Jul 31 '21	Oct 28 '21																							
278	Application and approval of TTA	167 days	Oct 1 '21	Mar 16 '22																							
279	Mainlaying by trenchless method	534 days	Jun 19 '23	Dec 3 '24																							
280	DN400, DN300 DI pipe (2 locations , total length 126m)	376 days	Jun 19 '23	Jun 28 '24	30																						
281	DN150 DI pipe (1 location , total length 33m)	158 days	Jun 29 '24	Dec 3 '24	15																						
282	Mainlaying by open trench method	230 days	Mar 17 '22	Nov 1 '22																							
283	DN400 DI pipe - 377m	230 days	Mar 17 '22	Nov 1 '22	30																						
284	Contractor's Design and Construction of distribution mains	1189 days	Oct 29 '21	Jan 29 '25																							
285	Submission and acceptance of detailed design proposal	120 days	Oct 29 '21	Feb 25 '22																							
286	Site investigation and liaison with relevant parties	120 days	Feb 26 '22	Jun 25 '22																							
287	Application of XP and TTA	120 days	Jun 26 '22	Oct 23 '22																							
288	Mainlaying by open trench method	820 days	Nov 2 '22	Jan 29 '25																							

Project: 3WSD20 Programme

Date: Nov 29 '21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split


Progress

Manual Progress


Page 6

Appendix D

Location of Designated Noise Monitoring Station CP-KTN-NMS5

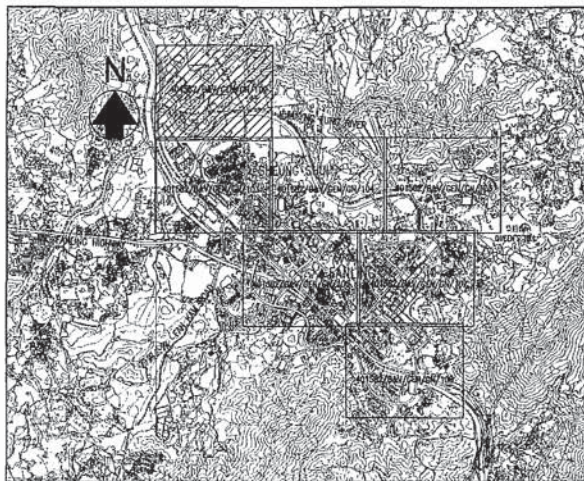

LOCATION PLAN
A1 1:10000
A3 1:20000

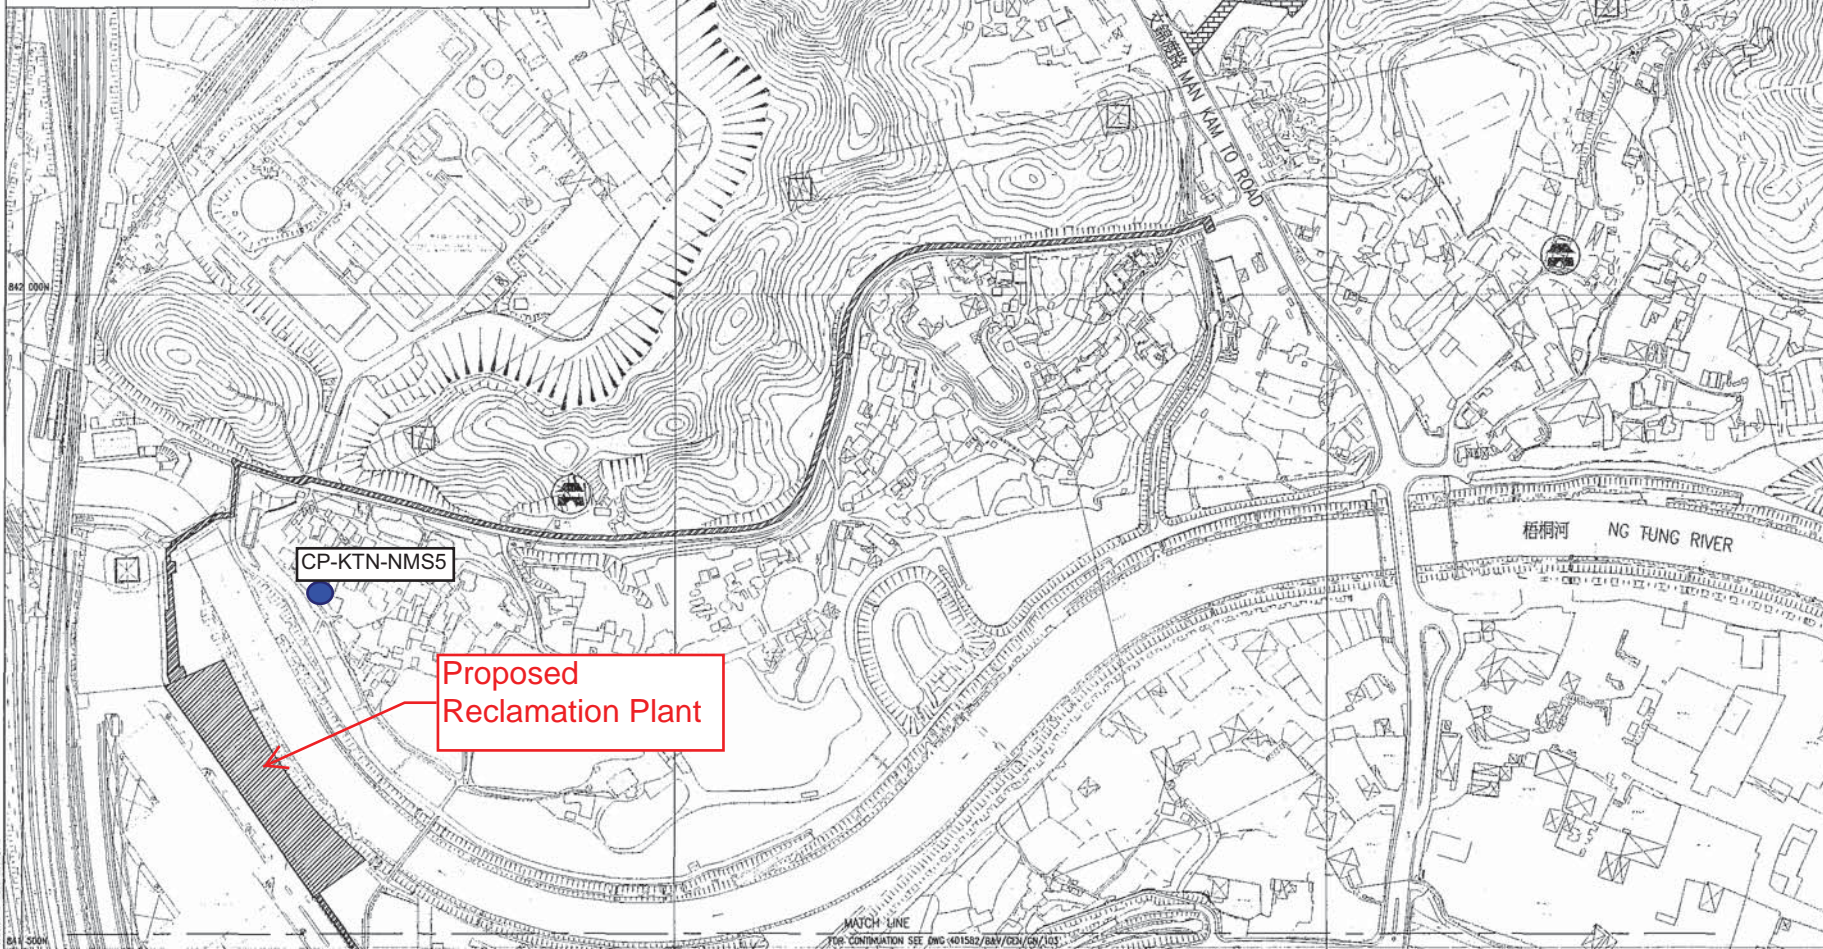

Copyright by Bechtel Hong Kong Limited

NOTES:

1. ALL LEVELS ARE IN REFERENCE TO METRES ABOVE THE HONG KONG PRINCIPAL DATUM (HKPD) UNLESS OTHERWISE STATED.
2. FOR GENERAL NOTES, REFER TO 401582/BAH/GEN/GN/001
3. ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE SPECIFIED.

COPYRIGHT RESERVED
THIS PRINT MAY NOT BE COPIED, TRACED, OR EXHIBITED WITHOUT PERMISSION OF THE WATER AUTHORITY.

1. THE BASE PLAN IS EXTRACTED FROM SURVEY SHEET NOS. 2-NE, 2-SZ, 3AW AND 3-SW.

LEGEND:

- PART 1 OF THE SITE
- PART 2 OF THE SITE
- PART 3 OF THE SITE
- PART 4 OF THE SITE
- PART 5 OF THE SITE
- PART 6 OF THE SITE
- PART 7 OF THE SITE
- PART W1 OF THE SITE

Revised	Date	Description	Drawn	Checked
Initial	CWC	WH	SZ	GC
Date	02/21	02/21	02/21	02/21

Approved

Contract No. 3/WSD/20

Contract Title

Reclaimed Water Supply to Sheung Shui and Fanling

Drawing Title

Noise Monitoring Station

Appendix E

Valid Calibration Certificates of Monitoring Equipment

Certificate of Calibration

校正證書

Certificate No. : C216479

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-2189)

Date of Receipt / 收件日期 : 25 October 2021

Description / 儀器名稱 : Sound Level Meter (EQ016)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00464681

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 9 November 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA


Tested By

測試


K P Cheuk
Project Engineer

Certified By

核證


K C Lee
Engineer

Date of Issue

簽發日期

10 November 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C216479
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C210084
CL281	Multifunction Acoustic Calibrator	AV210017

- Test procedure : MA101N.

- Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading	IEC 61672 Class 1 Spec.
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	93.6	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
30 - 130	L _A	A	Fast	94.00	1	93.6 (Ref.)
				104.00		103.6
				114.00		113.6

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading	IEC 61672 Class 1 Spec.
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	93.6	Ref.
			Slow			93.6	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C216479

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	67.3	-26.2 ± 1.5
					125 Hz	77.4	-16.1 ± 1.5
					250 Hz	84.9	-8.6 ± 1.4
					500 Hz	90.4	-3.2 ± 1.4
					1 kHz	93.6	Ref.
					2 kHz	94.8	+1.2 ± 1.6
					4 kHz	94.6	+1.0 ± 1.6
					8 kHz	92.6	-1.1 (+2.1 ; -3.1)
					16 kHz	85.7	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _C	C	Fast	94.00	63 Hz	92.7	-0.8 ± 1.5
					125 Hz	93.4	-0.2 ± 1.5
					250 Hz	93.6	0.0 ± 1.4
					500 Hz	93.6	0.0 ± 1.4
					1 kHz	93.6	Ref.
					2 kHz	93.5	-0.2 ± 1.6
					4 kHz	92.8	-0.8 ± 1.6
					8 kHz	90.7	-3.0 (+2.1 ; -3.1)
					16 kHz	83.7	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C216479

證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 17434

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Certificate of Calibration

校正證書

Certificate No. : C214361
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-1345)

Date of Receipt / 收件日期 : 8 July 2021

Description / 儀器名稱 : Sound Calibrator (EQ082)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 4231
Serial No. / 編號 : 2713428
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$
Line Voltage / 電壓 : ---

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 24 July 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By : 
測試 : K P Cheuk
Project Engineer

Certified By : 
核證 : K C Lee
Engineer

Date of Issue : 26 July 2021
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C214361
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C213954
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C201309

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Appendix F

Monitoring Schedule of the Reporting Month and Coming Month

The Reporting Monitoring Schedule (February 2022)

Date		Noise Monitoring (Leq30min)	Ecology Monitoring (Water Bird)
Tue	1-Feb-22		
Wed	2-Feb-22		✓ (Low Tide; High Tide on 31 Jan 2022)
Thu	3-Feb-22		
Fri	4-Feb-22	✓	
Sat	5-Feb-22		
Sun	6-Feb-22		
Mon	7-Feb-22		
Tue	8-Feb-22		
Wed	9-Feb-22		
Thu	10-Feb-22		✓ (Low Tide)
Fri	11-Feb-22	✓	✓ (High Tide)
Sat	12-Feb-22		
Sun	13-Feb-22		
Mon	14-Feb-22		
Tue	15-Feb-22		
Wed	16-Feb-22		✓ (Low Tide)
Thu	17-Feb-22	✓	✓ (High Tide)
Fri	18-Feb-22		
Sat	19-Feb-22		
Sun	20-Feb-22		
Mon	21-Feb-22		
Tue	22-Feb-22		
Wed	23-Feb-22	✓	
Thu	24-Feb-22		
Fri	25-Feb-22		✓ (High Tide)
Sat	26-Feb-22		✓ (Low Tide)
Sun	27-Feb-22		
Mon	28-Feb-22		

✓	Monitoring Day
	Sunday or Public Holiday

The Coming Month Monitoring Schedule (March 2022)

Date		Noise Monitoring (Leq30min)	Ecology Monitoring (Water Bird) ^{Note}
Tue	1-Mar-22	✓	
Wed	2-Mar-22		✓
Thu	3-Mar-22		
Fri	4-Mar-22		
Sat	5-Mar-22		
Sun	6-Mar-22		
Mon	7-Mar-22	✓	
Tue	8-Mar-22		✓
Wed	9-Mar-22		
Thu	10-Mar-22		
Fri	11-Mar-22		
Sat	12-Mar-22		
Sun	13-Mar-22		
Mon	14-Mar-22		
Tue	15-Mar-22		
Wed	16-Mar-22		
Thu	17-Mar-22		✓
Fri	18-Mar-22	✓	
Sat	19-Mar-22		
Sun	20-Mar-22		
Mon	21-Mar-22		
Tue	22-Mar-22		
Wed	23-Mar-22		✓
Thu	24-Mar-22	✓	
Fri	25-Mar-22		
Sat	26-Mar-22		
Sun	27-Mar-22		
Mon	28-Mar-22		
Tue	29-Mar-22		✓
Wed	30-Mar-22	✓	
Thu	31-Mar-22		

*Note:**Ecology monitoring dates are tentative and are subject to change*

✓	Monitoring Day
	Sunday or Public Holiday


Appendix G

Database of Monitoring Result

Daytime Noise Measurement Results (dB) at CP-KTN-NMS5																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Corrected Leq30min dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
4-Feb-22	11:02	58.4	61.5	56.5	60.8	63.5	58.0	61.2	63.5	58.0	62.0	63.0	56.5	61.0	64.5	52.0	60.4	61.0	55.0	60.8	63.8
11-Feb-22	9:03	59.7	60.6	57.9	59.4	60.6	57.9	58.6	59.6	57.5	58.3	59.4	57.2	58.8	60.2	57.4	58.4	59.7	57.1	58.9	61.9
18-Feb-22	9:31	61.7	65.0	58.6	60.2	61.5	58.2	60.2	61.4	58.8	59.8	61.7	57.4	60.3	62.8	56.4	59.3	61.0	57.3	60.3	63.3
23-Feb-22	9:57	57.8	59.5	56.0	58.1	60.2	55.8	55.9	57.0	54.7	56.0	57.2	54.5	55.4	56.9	54.1	56.4	58.1	54.0	56.7	59.7

Appendix H

Graphical Plots for Monitoring Result

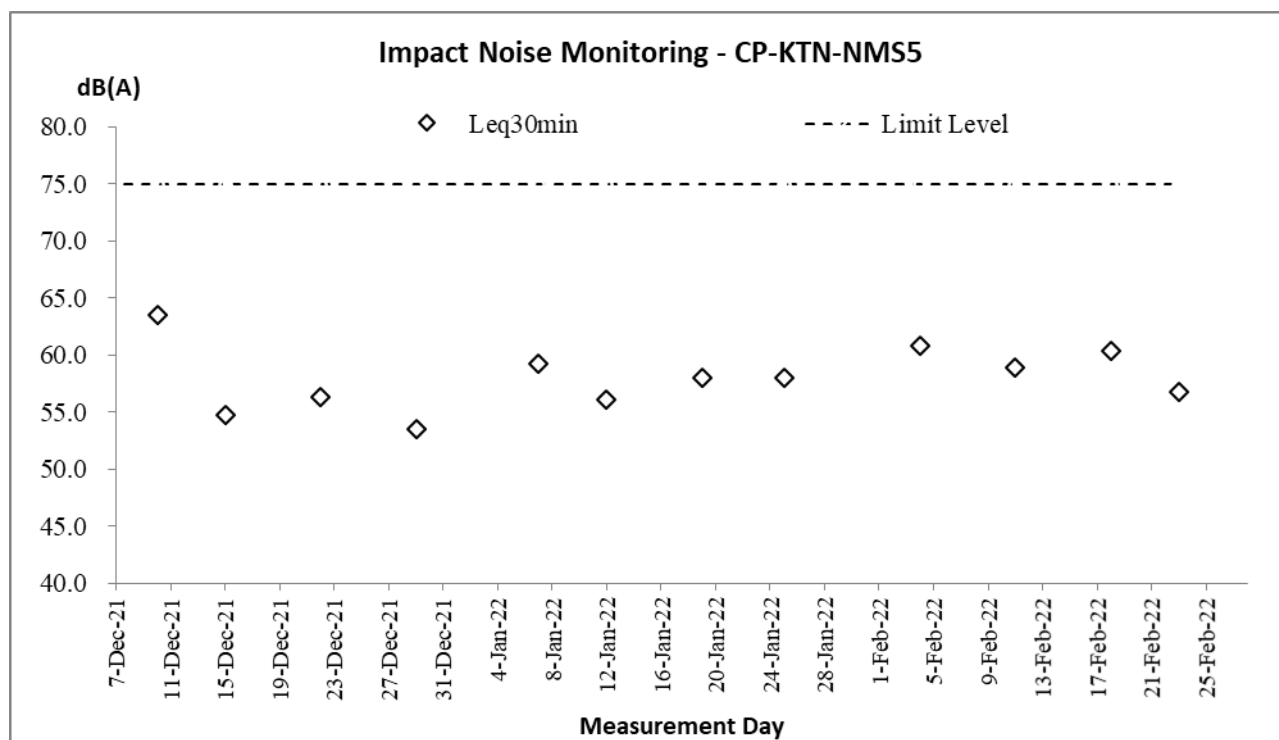

Appendix I

Monthly Summary Waste Flow Table

Contract No. : 3/WSD/20

Contact Name: Reclaimed Water Supply to Sheung Shui and Fanling**Monthly Summary Waste Flow Table for _2022_ (year)**

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	0.3031	0	0	0	0.3031	0	0	0	0	0	0.0016
Feb	0.5411	0	0	0	0.5411	0	0	0	0	0	0.0019
Mar											
Apr											
May											
June											
Sub-total	0.84429	0	0	0	0.84429	0	0	0	0	0	0.0035
July											
Aug											
Sept											
Oct											
Nov											
Dec											
Total	0.84429	0	0	0	0.84429	0	0	0	0	0	0.0035

Forecast of Total Quantities of C&D Materials to be Generated from the Contract*										
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
25.472	5.386	0	0	25.472	0	0	0	0	0	0.3885

Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material

Appendix J

Implementation Schedule for Environmental Mitigation Measures (ISEMM)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
Common Mitigation Measures (Applicable to ALL Project Components, including DPs and Non-DPs)							
Construction Dust Impact							
S3.8	D1	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road is proposed to achieve dust removal efficiency of 92.1%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.7 L/m ² to achieve the respective dust removal efficiencies.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO
S3.8	D2	The Contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO
S3.8	D3	<p>Following dust suppression measures should also be incorporated by the Contractor to control the dust nuisance throughout the construction phase:</p> <ul style="list-style-type: none"> Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not extend beyond the pedestrian barriers, fencing or traffic cones; The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle; Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hard cores; When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<ul style="list-style-type: none"> The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; Any skip hoist for material transport should be totally enclosed by impervious sheeting; and Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. 					
Noise Impact (Construction Phase)							
S4.9	N1	Implement the following good site management practices: <ul style="list-style-type: none"> only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; mobile plant should be sited as far away from NSRs as possible and practicable; and material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 	Control construction airborne noise	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N2	Install temporary site hoarding (approx. 2.4m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
			zone of NSRs through partial screening.				
S4.9	N3	Install movable noise barriers, full enclosure and acoustic mat, screen the noisy plants including air compressor and generator.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N4	Use of "Quiet" Plant and Working Methods	Reduce the noise levels of plant items	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N5	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
Water Quality Impact (Construction Phase)							
S5.7	W1	<p>Construction Runoff</p> <p>In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN 1/94), construction phase mitigation measures should be provided and the Storm Water Pollution Control Plan is given below.</p> <p>Storm Water Pollution Control Plan</p> <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the Contractor prior to the commencement of construction. Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications 	Control construction runoff	Contractor	All construction sites	Construction phase	WPCO, EIAO, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>where the influent is pumped.</p> <ul style="list-style-type: none"> • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates. • The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the Contractor prior to the commencement of construction. • Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. • All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas. • Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. • All open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. • Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. • Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff 					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>during storm events.</p> <ul style="list-style-type: none"> All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain. Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts. All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby. Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the meander, wetlands and fish ponds. 					
S5.7	W2	<p>Sewage from Workforce</p> <ul style="list-style-type: none"> Portable chemical toilets and sewage holding tanks should be provided for handling the construction sewage generated by the workforce. A licensed Contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause water quality impact after undertaking all required measures. 	Handling of site sewage	Contractor	All construction sites	Construction phase	WPCO, EIAO, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
Waste Management (Construction Waste)							
S7.6	WM1	<p>Waste Reduction Measures</p> <p>Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction:</p> <ul style="list-style-type: none"> • segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; • proper storage and site practices to minimize the potential for damage and contamination of construction materials; • plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; • sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); and • provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	All construction sites where practicable	Prior to the commencement of construction	Waste Disposal Ordinance
S7.6	WM2	Prepare Waste Management Plan and submit to the Engineer for approval	Minimize waste generation during construction	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM3	<p>Good Site Practice</p> <p>The following good site practices are recommended throughout the construction activities:</p> <ul style="list-style-type: none"> • nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; 	Minimize waste generation during construction	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM4	<p>Storage of Waste</p> <p>The following recommendation should be implemented to minimize the impacts:</p>	Minimize waste from storage impacts	Contractor	All construction	Construction phase	Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<ul style="list-style-type: none"> waste such as soil should be handled and stored well to ensure secure containment; stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; different locations should be designated to stockpile each material to enhance reuse; 			sites		
S7.6	WM5	Collection and Transportation of Waste The following recommendation should minimize the impacts: <ul style="list-style-type: none"> remove waste in timely manner; employ the trucks with cover or enclosed containers for waste transportation; obtain relevant waste disposal permits from the appropriate authorities; and disposal of waste should be done at licensed waste disposal facilities. 	Minimize waste from storage impacts	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM6	Excavated and C&D Material Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials: <ul style="list-style-type: none"> maintain temporary stockpiles and reuse excavated fill material for backfilling; carry out on-site sorting; deliver surplus artificial hard materials to Tuen Mun Area 38 recycling plant or its successor for recycling into subsequent useful products; make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; implement a recording system for the amount of waste generated, recycled and disposed of for checking; Standard formwork should be used as far as practicable in order to minimize the arising of C&D waste. The use of more durable formwork (e.g. metal hoarding) or plastic facing should be encouraged in order to enhance the possibility of recycling. The purchasing of construction materials should be carefully planned in order to avoid over ordering and wastage. Wheel wash facilities have to be provided at the site entrance before the trucks leaving the works area.	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005
S7.6	WM8	Chemical Waste <ul style="list-style-type: none"> If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producers. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical 	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal (Chemical Waste) General Regulation Code of Practice on the Packaging, Labelling and

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.					Storage of Chemical Waste
S7.6	WM9	General Waste <ul style="list-style-type: none"> General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal Ordinance
S7.6	WM10	Sewage <ul style="list-style-type: none"> The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities. Regularly collection by licensed collectors should be arranged to minimize potential environmental impacts. 	Minimize production of sewage impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal Ordinance
S7.6	WM11	Topsoil reuse – Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical. This is considered a general measure for good site practice.	Good site practice	Contractor / Project Proponent	Onsite	Construction Phase	<ul style="list-style-type: none"> ETWB Technical Circular (Works) No.29/2004
Landscape and Visual (Construction)							
S.12.9 MM3	LV5	Open Space Provision - the principles adopted in the RODP planning ensure that public open space systems are incorporated. All requirements for open space areas stipulated in the planning documents for the formulation of the Preliminary Layout Plan should be adhered to.	Reprovision of open space. Enhance visual amenity of the area and improve the overall landscape character	Government Developer / Detailed Design Consultant / Contractor	Onsite as stipulated in the planning documents for the formulation of the Preliminary Layout Plan	Prior to Construction and Construction Phase	Hong Kong Planning Standards and Guidelines (HKPSG) issued by the Planning Department (As at Aug 2011); Sustainable Building Design Guidelines
S.12.9 MM4	LV6	Tree Protection & Preservation – Existing trees to be retained within the Project Site should be carefully protected during construction. In particular OVTs will be preserved according to ETWB Technical Circular (Works) No. 29/2004. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to	Protect and Preserve Trees	Government Developer / Detailed Design Consultant / Contractor	Onsite as stipulated in the planning documents for the formulation of	Prior to Construction and Construction Phase	ETWB Technical Circular Works (TCW) No. 29/2004 and 3/2006

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>undertaking any works adjacent to all retained trees, including trees in Contractor's works areas.</p> <p>A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained.</p>			the Preliminary Layout Plan		
S.12.9 MM5	LV7	<p>Tree Transplantation – Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.</p> <p>A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBTC 2/2004 and 3/2006 and final locations of transplanted trees should be agreed prior to commencement of the work.</p> <p>For trees associated with highways e.g. roadside planting along highways, that are unavoidably affected and should be transplanted, HyD HQ/GN/13 'Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit' should be referred to.</p>	Transplant Trees where suitable for transplantation	Government Developer / Detailed Design Consultant / Contractor	Onsite where possible. Otherwise consider offsite locations	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWB TCW 3/2006 and 2/2004 HyD HQ/GN/13 Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit
S.12.9 MM7	LV9	<p>Compensatory Planting – Compensatory tree planting for felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Removal Application process under ETWBTC 3/2006.</p> <p>Compensatory planting is proposed at the potential open areas such as open spaces, amenity areas, open areas of the streetscapes, as well as the open areas within development lots.</p> <p>Compensatory planting for shrubs should be considered in suitable locations. Native species such as <i>Melastoma malabathricum</i>, <i>Diospyros vaccinioides</i>, <i>Gardenia jasminoides</i>, <i>Ixora chinensis</i>, <i>Ligustrum sinense</i>, <i>Litsea rotundifolia</i>, <i>Melastoma dodecandrum</i>, <i>Atalantia buxifolia</i>, <i>Rhodomyrtus tomentosa</i>, <i>Rhaphiolepis indica</i>, and <i>Rhododendron simsii</i> are suggested.</p>	Compensate for trees and shrubs lost due to the Project.	Government Developer / Detailed Design Consultant / Contractor	Onsite where possible. Otherwise consider offsite locations	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWB TCW 3/2006 and 2/2004
S.12.9 MM9	LV11	Vertical Greening – Planting of climbers to grow up vertical surfaces were appropriate (e.g. building edges, piers).	Soften hard surfaces and	Project Proponent /	On appropriate	Prior to Construction,	ETWB TCW No. 11/2004 – Cyber

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
			facilities	Detailed Design Consultant / Contractor / Maintenance Authority	structures	Construction Phase & Maintenance in Operation Phase	Manual for Greening
S.12.9 MM10	LV12	Green Roof – Roof greening where appropriate should be established on proposed buildings as per the guidelines stated. These guidelines provide further details including information regarding structural loading, design, maintenance, etc. considerations as well as providing information on what types of plants might be suitable.	Reduce exposure to untreated concrete surfaces and particularly mitigate visual impact to VSRs at high levels. Provide greening.	Project Proponent / Detailed Design Consultant / Contractor / Maintenance Authority	On appropriate buildings	Prior to Construction, Construction Phase & Maintenance in Operation Phase	CIBSE HK Branch, Technical Guidelines for Green Roof Systems in Hong Kong (2011); ArchSD/Urbis Study on Green Roof Application in HK (2007)
S.12.9 MM11	LV13	Screen Planting – Tall screen/buffer trees and shrubs should be planted. This measure may additionally form part of the compensatory planting.	To screen proposed structures such as roads and buildings. Improve compatibility with the surrounding environment and create a pleasant pedestrian environment	Government / Developer / Detailed Design Consultant / Contractor	Along roads, around suitable built structures, or around VSRs to contain their view out to the NDA Maintenance and create a pleasant Contractor structures	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWBTC 3/2006
S12.9 MM14.5	LV20	Screen Hoarding – Screen hoarding shall be erected along areas of the construction works site boundary where the works site borders publically accessible routes and/or is close to visually sensitive receivers (VSRs). It is proposed that the screening be compatible with the surrounding environment and where possible, nonreflective, recessive colours be used. Any works areas near the ecological sensitive areas should erect 2m high dull green site boundary fence. Details can refer to the ecological impact assessment (Chapter 13 of the EIA report).	To screen undesirable views of the works site.	Contractor	Throughout NDAs	Construction Phase	
S12.9	LV21	Light Control – Construction day and night time lighting should be controlled to	To minimize glare	Government /	Throughout	Construction	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
MM14.6		minimize glare impact to adjacent VSRs during the Construction phase. Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase.	impact to adjacent VSRs	Developer / Contractor	NDA's	and Operation Phases	
Ecology (Construction Phase)							
S.13.9	E13	Review design and construction methods for bridges, especially those on the Sheung Yue and tidal Ng Tung Rivers, and adopt measures which minimize impacts on rivers and disturbance and fragmentation impacts on fauna. No construction during ardeid breeding season (1 March to 31 July) along Sheung Yue River north and east of KTN area D1-5 and east of D1-9 and C2-3 and restriction of working hours on new pedestrian bridges over the Sheung Yue River and tidal Ng Tung River to 09.00 to 17.30 during the ardeid breeding season (1 March to 31 July). Provision of alternative foraging habitat along main river channels for large waterbirds.	Minimize impacts on rivers and disturbance and fragmentation impacts on fauna.	Project Proponent / Detailed Design Consultant / Contractor	Along and within the Sheung Yue, Ng Tung and Shek Sheung Rivers	Detailed design and construction phases.	TM-EIAO.
S.13.9	E16	Creation of Green Corridors along the Sheung Yue, Ng Tung and Shek Sheung Rivers, retention and provision of screen plantings where feasible; provision of Open Space areas and development areas along river corridors; Design and erection of 2m high solid dull green site barrier fence between river channel and any active works area along or adjacent to Ng Tung, Sheung Yue and Shek Sheung Rivers. Ng Tung, Sheung Yue and Shek Sheung Rivers screen planting.	Minimize disturbance to waterbirds using Ng Tung, Sheung Yue and Shek Sheung River channels.	Detailed Design Consultant / Contractor	Ng Tung, Sheung Yue and Shek Sheung Rivers	Detailed design and construction phases.	TM-EIAO.
S.13.9	E19	Use opaque, non-transparent, non-reflective noise barriers for all construction sites. Unnecessary lighting should be avoided.	Minimize mortality impacts on birds.	Contractor	All construction sites	Construction phase.	TM-EIAO.

Appendix K

Waterbirds Survey Report for the Reporting Month



**WSD Contract No. 3/WSD/20 - Reclaimed Water Supply to
Sheung Shui and Fanling - Provision of EM&A (Ecological)
Monitoring**

Monthly Report for February 2022
(Issue 1)



Job Ref.: 21/2063/582 AUES-SWHTSE
Date: 14th March 2022

WSD Contract No. 3/WSD/20 - Reclaimed Water Supply to Sheung Shui and Fanling - Provision of EM&A (Ecological) Monitoring

Monthly Report for February 2022

(Issue 1)

March 2022

	Name	Signature
Prepared by:	Nicholas Tam	
Reviewed by:	Ida Yu	
Date:	14th March 2022	

CONTENTS

1	Introduction	1
2	Monitoring Methodology	1
3	Analytical methodology	2
4	Results	3
5	Analysis	4
6	Observations	5
7	References	6

LIST OF TABLES

Table 1	Ecological Monitoring Stations
Table 2	Representative Waterbirds
Table 3	Action and Limit Levels and Responses to Evidence of Disturbance to Waterbirds using Ng Tung, Sheung Yue and Shek Sheung Rivers during Construction Phase
Table 4	Weather Conditions and Tidal Information of Survey Dates in February 2022
Table 5	Total Bird Species and Abundance in the Reporting Month
Table 6	Abundance of Representative Waterbirds in the Reporting Month
Table 7	T-test Result for Waterbirds in the Reporting Month
Table 8	Noise Level Measured at NMS5 in February 2022
Table 9	Observations during the Ecological Monitoring in the Reporting Month

LIST OF APPENDICES

Appendix A	Recorded Bird Species and their Abundance in the Reporting Month
Appendix B	Total Waterbird Abundance from Point Count
Appendix C	Abundance of Representative Waterbirds from Point Count
Appendix D	Survey Photos

LIST OF FIGURES

Figure 1	Transect and Point Count Locations
Figure 1a	Transect and Point Count Locations (Zoomed In)

1 INTRODUCTION

- 1.1 According to the Section 12.3.2.5 of “Updated EM&A Manual for Advance And First Stage Works of Kwu Tung North and Fanling North New Development Areas”, monitor of measures to minimise disturbance to waterbirds on Ng Tung, Sheung Tue and Shek Sheung Rivers is required.
- 1.2 aec Ltd. has been appointed by Action-United Environmental Services & Consulting (AUES) to: conduct weekly transect bird surveys at high and low tides along Ng Tung River, Sheung Yue River and Shek Sheung River; and identify sources of actual and potential disturbances to birds due to construction activities of WSD Contract No. 3/WSD/20 – Reclaimed Water Supply to Sheung Shui and Fanling. As instructed by the Contractor, the commencement date of the survey was in the week of 10th January 2022. This monthly report summarises the monitoring findings in February 2022.

2 MONITORING METHODOLOGY

- 2.1 The survey methodology references the methodology stated in approved Baseline Monitoring Report (Ecology) (Version 1) (prepared by Cinotech Consultants Limited (2019)) under “Contract No. SPW 08/2019 – Shek Wu Hui Effluent Polishing Plant – Main Works Stage 1”. Three transects and seven point count locations were selected within the 500m boundary of Ng Tung, Sheung Yue and Shek Sheung River. These locations are shown in **Figure 1** and summarized in **Table 1**.

Table 1 Ecological Monitoring Stations

Monitoring Stations	Descriptions	Influenced by Tidal Action
Transect T1	Along Ng Tung River	No
Transect T2		
Point Count Location P1		
Point Count Location P2		
Point Count Location P3		
Point Count Location P4		
Point Count Location P5	At Shek Sheung River (Low-flow Channel)	No
Transect T3	Along Shek Sheung River & Sheung Yue River	Yes
Point Count Location P3	At Shek Sheung River	Yes
Point Count Location P3	At Intersection between Sheung Yue and Shek Sheung River	Yes

- 2.2 Surveys were conducted on a weekly basis at both high and low tides (it is considered high tide when tidal levels are above 1.5m and low tide when tidal level are below 1.5m at Tsim Bei Tsui Station).
- 2.3 All avifauna species that were seen or heard were identified and quantified along transects and at point count locations. Survey data would be recorded continuously by the surveyor as they walk along the transects, while survey data of each point count location would be collected for 5-minutes after surveyor reaches the designated point count location. During

the surveys, the utilisation of Ng Tung River, Sheung Yue River and Shek Shui River and their immediate environs/habitats by waterbirds will be focused. For comparison and data analysis, the transect routes and point count locations follows Figure 1 of the approved Baseline Monitoring Report (Ecology) (Version 1).

- 2.4 Noticeable behaviours such as breeding, nesting, roosting, feeding and presences of recently fledged juveniles were recorded and reported. In the case which such behaviours were observed for species of conservation importance, the Resident Engineer (RE), the Contractor and the Independent Environmental Checker (IEC) would be immediately notified after the survey such that the Contractor could review the current construction programme and minimize disturbances due to construction activities.
- 2.5 Weather conditions, tidal information, time of the survey and other noticeable activities occurring within the vicinity of the survey area were recorded.

3 ANALYTICAL METHODOLOGY

- 3.1 Total number of waterbirds and six representative waterbird species (listed in **Table 2**) are used as an indicator of the level disturbance to water birds at each of the survey location. Species listed as wetland-dependant according to Carey *et al.* (2001) are defined as waterbirds. A significant decline in the abundance of all or representative waterbirds would indicate a high level of disturbance.

Table 2 Representative Waterbirds

Common Name	Species Name	Chinese Name
Chinese Pond Heron	<i>Ardeola bacchus</i>	池鷺
Eastern Cattle Egret	<i>Bubulcus coromandus</i>	牛背鷺
Grey Heron	<i>Ardea cinerea</i>	蒼鷺
Great Egret	<i>Ardea alba</i>	大白鷺
Little Egret	<i>Egretta garzetta</i>	小白鷺
Great Cormorant	<i>Phalacrocorax carbo</i>	普通鸕鶿

- 3.2 Survey data from each month is compared to the baseline monitoring data. When a decline in the total number of Waterbirds or the number of the representative Waterbird species is recorded the survey data would be compared to the baseline data (from Shek Wu Hui Effluent Polishing Plant Baseline Monitoring Report (Ecology) by Cinotech Consultants Limited, 2019) using a two-sample one-tailed Student's t-test assuming unequal variance to analyse whether the decline is significant.
- 3.3 If the collected data for the reporting month shows a significant difference at the 95% confidence level, the action level will be triggered. If the collected data for the reporting month shows a significant difference at the 99% confidence level, the limit level is triggered and corresponding suggestions would be given to minimize the disturbances according to **Table 3**.

Table 3 Action and Limit Levels and Responses to Evidence of Disturbance to Waterbirds using Ng Tung, Sheung Yue and Shek Sheung Rivers during Construction Phase

Action Level	Response	Limit Level	Response
Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Action Level response is triggered.	Investigate cause(s) and if cause(s) identified as related to NDAs project instigate remedial action to remove or reduce source of disturbance.	Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Limit Level response is triggered.	Investigate cause(s) and if cause(s) identified as related to the NDAs project instigate remedial action. Review and adjust project's Long Valley Nature Park (LVNP) management measures to improve conditions for affected species.
Decline in numbers of any one Waterbird species occurring in significant numbers* during Baseline Monitoring such that the Action Level response is triggered.	Investigate cause(s) and if cause(s) identified as related to NDAs project instigate remedial action to remove or reduce source of disturbance.	Decline in numbers of any one Waterbird species occurring in significant numbers* during Baseline Monitoring such that the Limit Level response is triggered.	Investigate cause(s) and if cause(s) identified as related to the NDAs project instigate remedial action. Review and adjust project's LVNP management measures to improve conditions for affected species.

Note: Whether numbers are significant depend on species and season after collection and evaluation of baseline survey data.

- 3.4 In order to increase the sample size and reduce the random error on each survey day, survey data would be collectively analysed on a monthly basis. The collective data of each month is also compared to the baseline data of the respective month and season instead of the entire data set, to account for the seasonal variation in the abundance of waterbirds. In this study, the Winter season is defined as October to March, while the Summer season is defined as April to September.

4 RESULTS

- 4.1 The weather conditions and tide levels on the survey dates are listed in the table below.

Table 4 Weather Conditions and Tidal Information of Survey Dates in February 2022

High Tide				Low Tide			
Date	Time	Tide (m)	Weather	Date	Time	Tide (m)	Weather
31-1-2022	13:00	2	Cloudy	2-2-2022	10:00	1.5	Cloudy
11-2-2022	14:00	1.7	Sunny	10-2-2022	10:00	1.2	Cloudy
17-2-2022	11:00	1.64	Cloudy	16-2-2022	8:45	1.3	Sunny
25-2-2022	12:00	1.5	Sunny	26-2-2022	11:00	1.44	Sunny

- 4.2 Abundance and diversity of key species are summarized in **Table 5** and **Table 6**. Detailed list of avifauna recorded is provided in **Appendix A**.

Table 5 Total Bird Species and Abundance in the Reporting Month

Category	Number of Species	Abundance
All Avifauna	49	402
Waterbirds	16	151

Table 6 Abundance of Representative Waterbirds in the Reporting Month

Common Name	Species Name	Chinese Name	Abundance
Chinese Pond Heron	<i>Ardeola bacchus</i>	池鷺	11
Eastern Cattle Egret	<i>Bubulcus coromandus</i>	牛背鷺	11
Grey Heron	<i>Ardea cinerea</i>	蒼鷺	23
Great Egret	<i>Ardea alba</i>	大白鷺	32
Little Egret	<i>Egretta garzetta</i>	小白鷺	38
Great Cormorant	<i>Phalacrocorax carbo</i>	普通鸕鶿	11

5 ANALYSIS

- 5.1 The result of Student's t-test for all waterbirds and representative waterbirds are compiled in **Table 7** respectively. Further details are provided in **Appendices B** and **C**.

Table 7 T-test Result for Waterbirds in the Reporting Month

Category	Monthly					Seasonal				
	T-value	df	p	Action Level	Limit Level	T-value	df	p	Action Level	Limit Level
All Waterbirds	-2.323	9	0.022	*		-4.104	8	0.002	*	*
Chinese Pond Heron	-3.223	10	0.005	*	*	-5.700	9	0.000	*	*
Eastern Cattle Egret	No decline					-0.973	41	0.168		
Grey Heron	-5.363	9	0.000	*	*	-5.980	18	0.000	*	*
Great Egret	No decline					No decline				
Little Egret	-2.265	6	0.032	*		-3.691	5	0.007	*	*
Great Cormorant	No decline					No decline				

* = level triggered

- 5.2 While the numbers of Eastern Cattle Egret, Great Egret and Little Egret are all on a similar level compared to the baseline data; the low number of waterbirds as a whole, Chinese Pond Heron, Grey Heron, Little Egret and Great Cormorant all trigger the limit level on at least one calculation method.
- 5.3 The data indicates that in general, number of waterbirds at the study area is significantly lower compared to the baseline data. The surveyor identified sources of disturbances to be fishing activities at all transects (that may scare birds away from foraging with vicinity of fishermen), the discharge of sewage water at P3, and the higher level of noise generated from different construction activities surrounding T2 (which does not belong to the construction site under the Contract). Relevant photos are shown in **Appendix D**.
- 5.4 Noise level monitoring data in February 2022 of the Noise Monitoring Spot (NMS5) for the current Project was checked (Noise Level for February 2022 is provided in **Table 8**). The level

fluctuated between a minimum of 59.7dB and a maximum of 63.8dB between the monitoring weeks, but never exceeded the limit level of 75dB. This indicates that although noise level was considerably high as reported by the surveyor (and may have disincentivized birds to forage at T1 and T2), it is still at an acceptable level. However, the cumulative noise disturbance from different construction sites along the surveyed rivers could not be ruled out.

Table 8 Noise Level Measured at NMS5 in February 2022

Date	Start Time	Corrected Leq 30 min	Limit Level
4-Feb-22	9:17	63.8	75.0
11-Feb-22	9:03	61.9	75.0
18-Feb-22	9:31	63.3	75.0
23-Feb-22	9:57	59.7	75.0

- 5.5 Aside from immediate sources of disturbances, it is suggested that the change in habitat of LVNP might also have caused a difference in composition and abundance of species that visit its nearby areas for several reasons: birds might be more attracted to forage within LVNP instead due to enhanced habitats; or the change in habitats (abandoned agricultural lands to various wetland habitats) within LVNP has attracted a group of species with a different niche to the surrounding areas. Although, this hypothesis could not be entirely proven as bird data within LVNP is not given.
- 5.6 The change of the abundance of certain representative waterbirds is still under investigation, but a clearer cause for the reduction in waterbird abundance could not be identified, and we could only theorize that the cumulative impacts of human disturbances and change in the surrounding habitats (including LVNP) are related to the decrease in waterbirds.
- 5.7 By reviewing the recent two Monthly EM&A Reports (December 2021 and January 2022) under *Contract No. SPW 12/2021 Shek Wu Hui Effluent Polishing Plant – Main Works*, both reports stated that no action and limit levels were triggered by comparing their waterbird abundance with the baseline monitoring dataset. While the difference of the monitoring findings between this Project and DSD's Project will be further investigated (e.g. survey transect routes and point count locations), the findings from DSD's EM&A Reports can reflect there is no significant impact from the current Project which has been commenced since December 2021.
- 5.8 However, since the current monitoring findings have triggered the action and/or limit levels, it is suggested that the construction site should continue keeping the best site practice in noise control to minimize disturbance caused to waterbirds. Surveyors would also pay special attention to the types of construction works in relation to noise creation and how nearby waterbirds have responded to the activities.

6 OBSERVATIONS

- 6.1 Waterbird behavior observed during ecological monitoring is listed below:
- Flying
 - Resting
 - Foraging

6.2 The anthropogenic activities observed during ecological monitoring is listed in **Table 9**

Table 9 Observations during the Ecological Monitoring in the Reporting Month

Location	Observations
T1 (PC1, PC2)	Fishing
T2 (PC3, PC4)	Fishing
T3 (PC6, PC7)	Fishing

7 REFERENCES

Carey, G.J., Chalmers, M.L., Diskin, D.A., Kennerley, P.R., Leader, P.J., Leven, M.R., Lewthwaite, R.W., Melville, D.S., Turnbull, M., and Young, L. 2001. The Avifauna of Hong Kong. Hong Kong Bird Watching Society, Hong Kong.

Cinotech Consultants Limited. 2019. Shek Wu Hui Effluent Polishing Plant Baseline Monitoring Report (Ecology). Accessed from https://shekwuhui.cinotech.hk/?page_id=24 in Jan 2022.

Cinotech Consultants Limited. 2019. Contract No. SPW 08/2019 Shek Wu Hui Effluent Polishing Plant – Main Works Stage 1 Baseline Monitoring Report (Ecology) (Version 1). Accessed from https://shekwuhui.cinotech.hk/?page_id=24 in Jan 2022.

Appendix A Recorded Bird Species and their Abundance in the Reporting Month

Common Name	Chinese Name	Scientific Name	Waterbird	Point Count Abundance	Transect Abundance
Black-crowned Night Heron	夜鷺	<i>Nycticorax nycticorax</i>	Y		+
Chinese Pond Heron	池鷺	<i>Ardeola bacchus</i>	Y	11	++
Eastern Cattle Egret	牛背鷺	<i>Bubulcus coromandus</i>	Y	11	+
Grey Heron	蒼鷺	<i>Ardea cinerea</i>	Y	23	+++++
Great Egret	大白鷺	<i>Ardea alba</i>	Y	32	++++
Little Egret	小白鷺	<i>Egretta garzetta</i>	Y	38	+++++
Great Cormorant	普通鸕鶿	<i>Phalacrocorax carbo</i>	Y	11	+++
Besra	松雀鷹	<i>Accipiter virgatus</i>	N	1	
Black Kite	黑鳶	<i>Milvus migrans</i>	N	1	+
Eastern Buzzard	普通鳶	<i>Buteo japonicus</i>	N	1	
White-breasted Waterhen	白胸苦惡鳥	<i>Amaurornis phoenicurus</i>	Y		+
Black-winged Stilt	黑翅長腳鷗	<i>Himantopus himantopus</i>	Y	6	+
Pied Avocet	反嘴鷗	<i>Recurvirostra avosetta</i>	Y	3	+
Common Sandpiper	磯鷗	<i>Actitis hypoleucos</i>	Y	1	+
Common Greenshank	青腳鷗	<i>Tringa nebularia</i>	Y	8	++
Spotted Dove	珠頸斑鳩	<i>Spilopelia chinensis</i>	N	22	+++
House swift	小白腰雨燕	<i>Apus nipalensis</i>	N	10	+++
White-throated Kingfisher	白胸翡翠	<i>Halcyon smyrnensis</i>	Y	4	+
Common Kingfisher	普通翠鳥	<i>Alcedo atthis</i>	Y	1	+
Pied Kingfisher	斑魚狗	<i>Ceryle rudis</i>	Y		+
Long-tailed Shrike	棕背伯勞	<i>Lanius schach</i>	N	1	+
Hair-crested Drongo	髮冠卷尾	<i>Dicrurus hottentottus</i>	N		+
Red-billed Blue Magpie	紅嘴藍鵲	<i>Urocissa erythroryncha</i>	N		+
Oriental Magpie	喜鵲	<i>Pica serica</i>	N	8	+
Collared Crow	白頸鴉	<i>Corvus torquatus</i>	Y	2	+
Large-billed Crow	大嘴烏鴉	<i>Corvus macrorhynchos</i>	N		+
Cinereous Tit	蒼背山雀	<i>Parus cinereus</i>	N	6	+
Red-whiskered Bulbul	紅耳鶇	<i>Pycnonotus jocosus</i>	N	12	+
Chinese Bulbul	白頭鶇	<i>Pycnonotus sinensis</i>	N	6	+
Barn Swallow	家燕	<i>Hirundo rustica</i>	N	40	+++++
Yellow-browed Warbler	黃眉柳鶯	<i>Phylloscopus inornatus</i>	N	36	+++++
Pallas's leaf Warbler	黃腰柳鶯	<i>Phylloscopus proregulus</i>	N	7	++
Dusky Warbler	褐柳鶯	<i>Phylloscopus fuscatus</i>	N		+
Yellow-bellied Prinia	黃腹鷦鶯	<i>Prinia flaviventris</i>	N	11	++
Common Tailorbird	長尾縫葉鶯	<i>Orthotomus sutorius</i>	N		+
Masked Laughingthrush	黑臉噪鷓	<i>Pterorhinus perspicillatus</i>	N	14	+++
Swinhoe's white-eye	暗綠繡眼鳥	<i>Zosterops simplex</i>	N	13	+++++
Crested Myna	八哥	<i>Acridotheres cristatellus</i>	N	29	+++++
Black-collared Starling	黑領椋鳥	<i>Gracupica nigricollis</i>	N	5	+
Oriental Magpie Robin	鵲鵲	<i>Copsychus saularis</i>	N	2	+
Asian Brown Flycatcher	北灰鶇	<i>Muscicapa dauurica</i>	N		+

Common Name	Chinese Name	Scientific Name	Waterbird	Point Count Abundance	Transect Abundance
Red-throated Flycatcher	紅喉姬鵯	<i>Ficedula albicilla</i>	N		+
Daurian Redstart	北紅尾鴝	<i>Phoenicurus aureus</i>	N	2	+
Stejneger's Stonechat	黑喉石(即鳥)	<i>Saxicola stejnegeri</i>	N	1	+
Fork-tailed Sunbird	叉尾太陽鳥	<i>Aethopyga christinae</i>	N		+
Scaly-Breasted Munia	斑文鳥	<i>Lonchura punctulata</i>	N		++
Eastern Yellow Wagtail	東黃鵪鶉	<i>Motacilla tschutschensis</i>	N	1	
White Wagtail	白鵪鶉	<i>Motacilla alba</i>	N	20	+++
Olive-backed Pipit	樹鵪	<i>Anthus hodgsoni</i>	N	2	++
Total Point Count Abundance				402	
Total Waterbirds				151	

For transect abundance, +: 1-10, ++: 11-20, +++: 21-30, ++++: 31-40, +++++: >40

Appendix B Total Waterbird Abundance from Point Count

Survey Information				Number of Waterbirds	
Week	Date	Time	Tide Level	Individuals Recorded	Total
1	31-Jan-22	13:00	High	21	33
	2-Feb-22	10:00	Low	12	
2	11-Feb-22	14:00	High	8	28
	10-Feb-22	10:00	Low	20	
3	17-Feb-22	11:00	High	17	47
	16-Feb-22	8:45	Low	30	
4	25-Feb-22	12:00	High	11	43
	26-Feb-22	11:00	Low	32	
				Survey Average	37.75
				February Average	61
				Winter Average	60.77

Appendix C Abundance of Representative Waterbirds from Point Count

Representative Species		Recorded Abundance						Baseline	
Common Name	Species Name	Week 1	Week 2	Week 3	Week 4		Average	February Average	Winter Average
Chinese Pond Heron	<i>Ardeola bacchus</i>	3	1	2	5		2.75	8.13	9.21
Eastern Cattle Egret	<i>Bubulcus coromandus</i>	2	3	3	3		2.75	2.38	3.77
Grey Heron	<i>Ardea cinerea</i>	3	3	5	0		2.75	15.75	12.82
Great Egret	<i>Ardea alba</i>	7	6	11	8		8	4.38	5.15
Little Egret	<i>Egretta garzetta</i>	11	1	5	6		5.75	11.5	14.36
Great Cormorant	<i>Phalacrocorax carbo</i>	2	13	11	12		9.5	8.63	7.08

Appendix D Survey Photos

Photo 1 Fishing activities at Transect 1

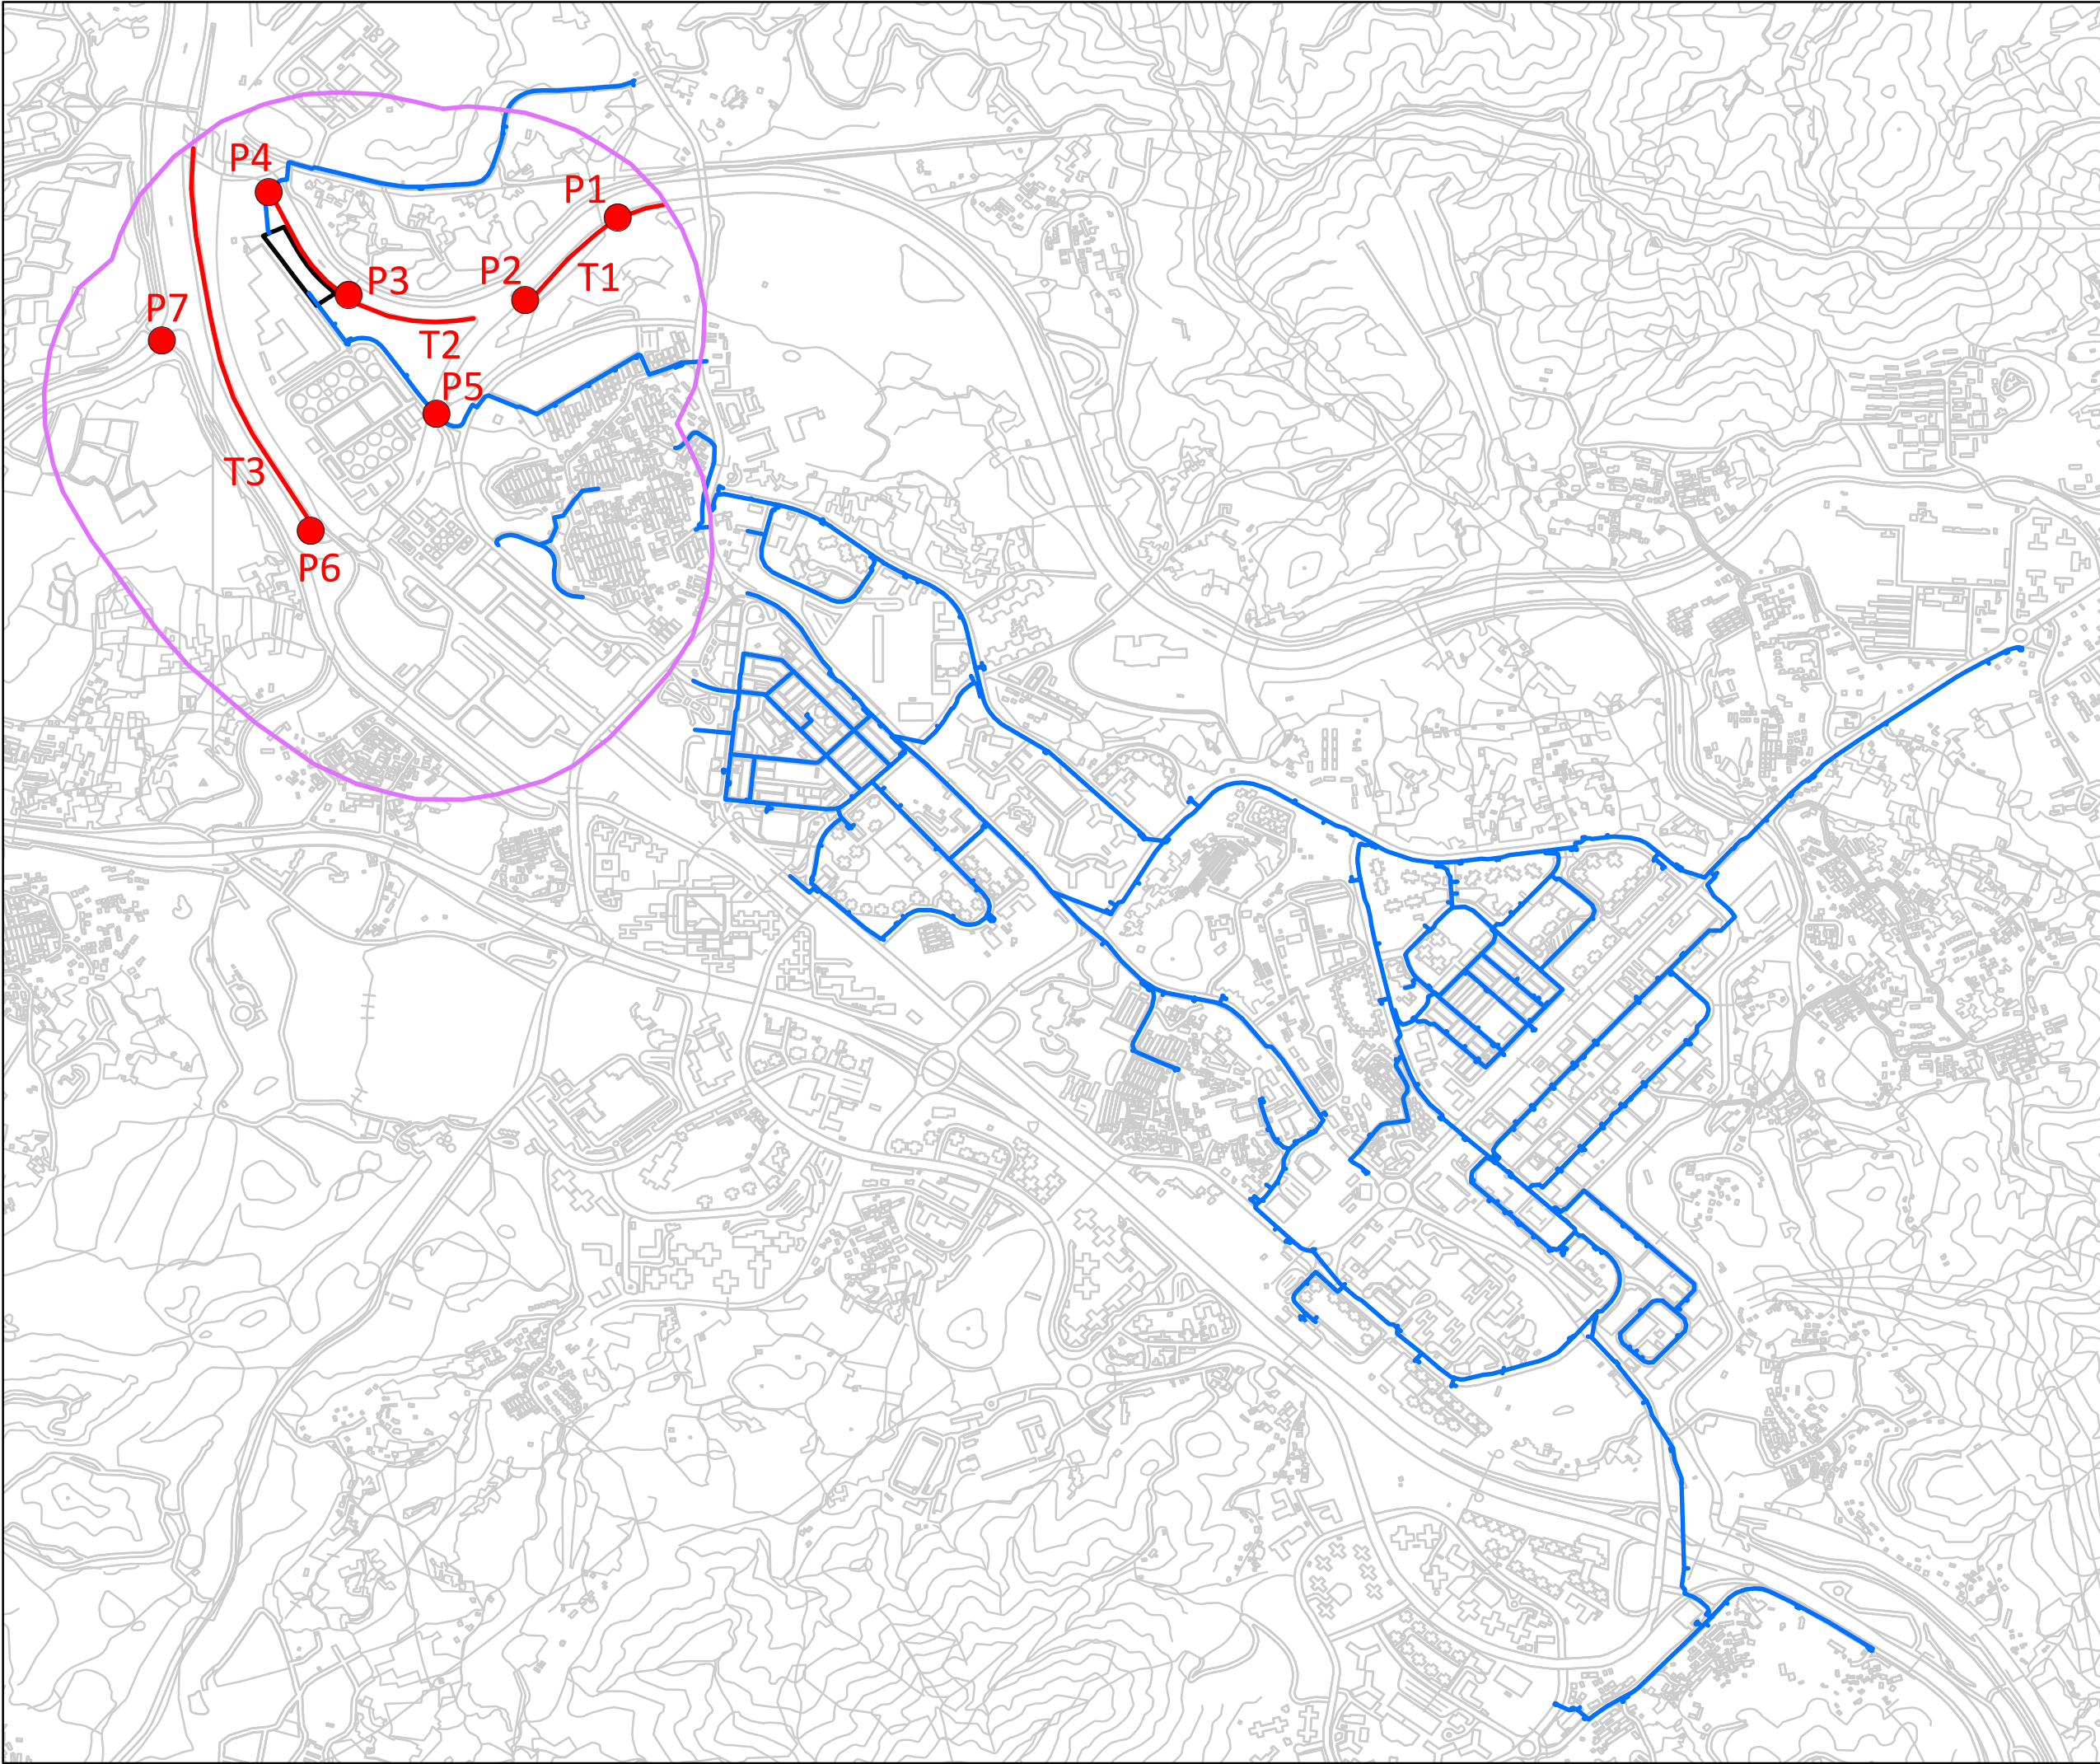


Photo 2 Construction sites and lamb grazing at Transect 2



Figure 1

Transect and Point Count Locations



- Proposed Shek Wu Hui Water Reclamation Plant
- 500m Survey Boundary
- Proposed Retained Water Mains
- Walk Transect
- Point Count Locations



Project Title:

WSD Contract No. 3/WSD/20 -
Reclaimed Water Supply to Sheung Shui and Fanling -
Provision of EM&A (Ecological) Monitoring


Figure Title:

Transect and Point Count Locations

Drawn by:	JH	Scale:	1:14,500	on A3
Checked By:	NT	Date:	11 Mar 2022	
Approved by:	iy			
Figure Number:	Figure 1			Revision: 1

Figure 1a

Transect and Point Count Locations (Zoomed In)

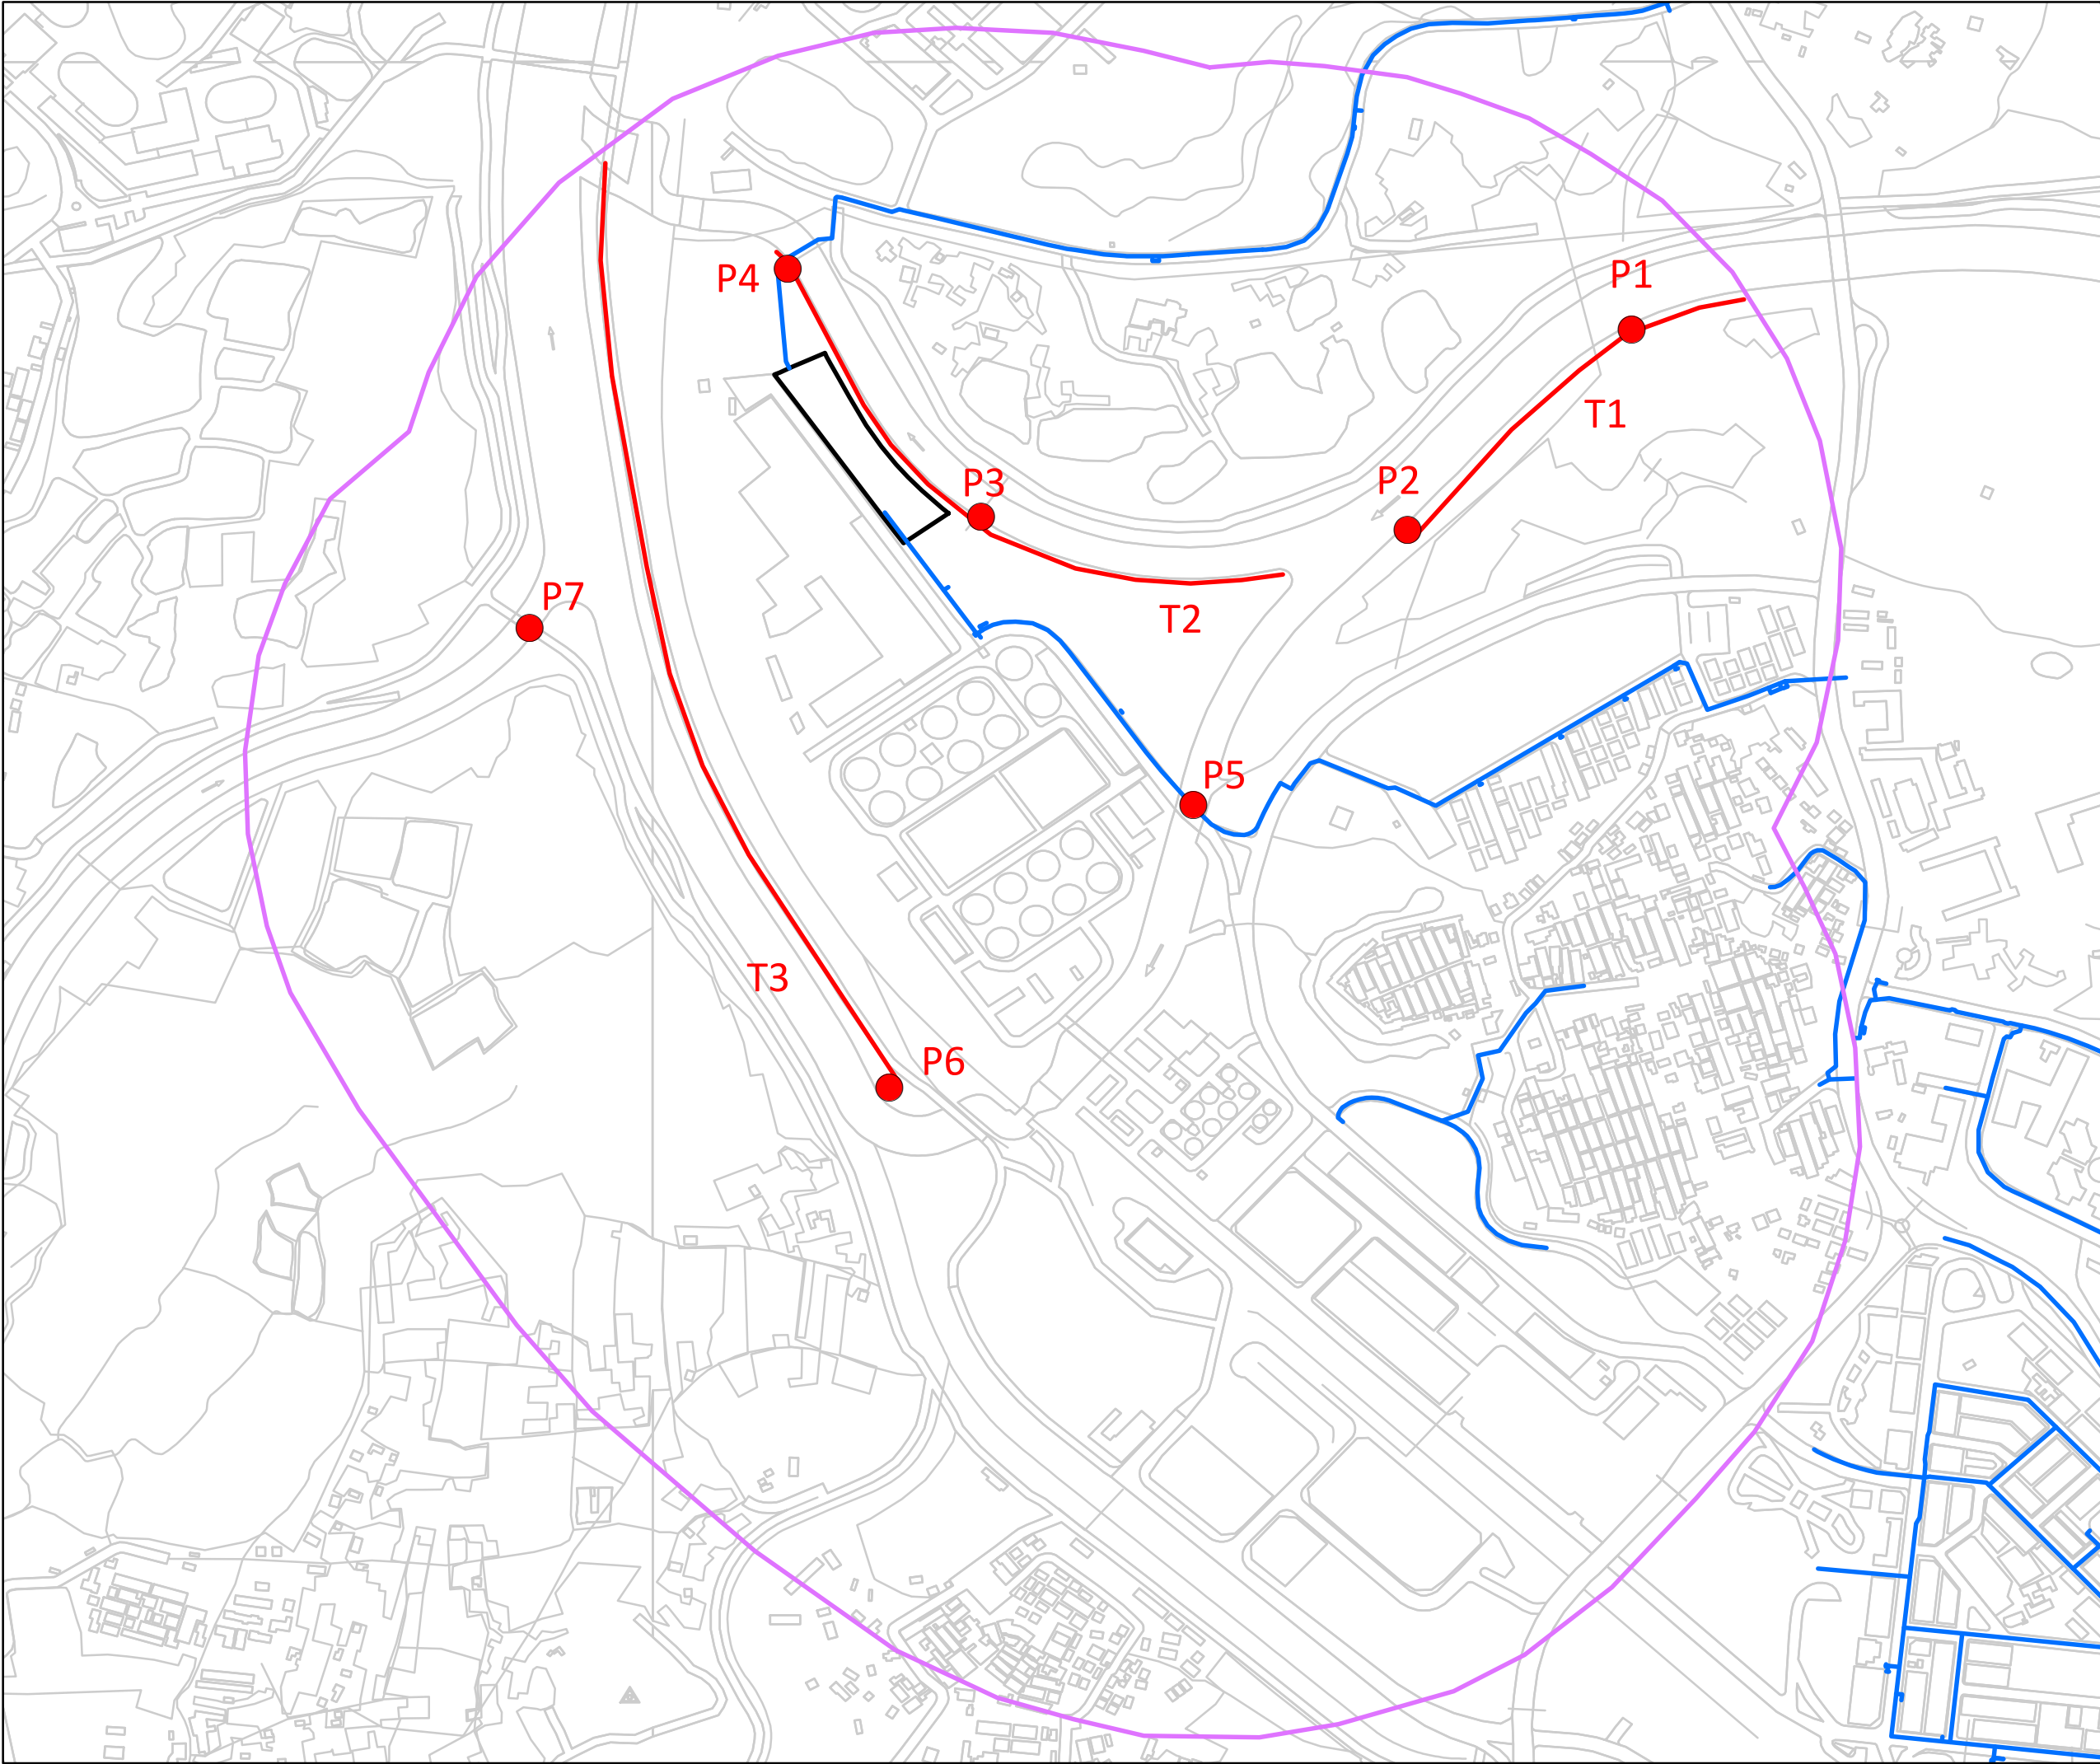

- Proposed Shek Wu Hui Water Reclamation Plant
- 500m Survey Boundary
- Proposed Retained Water Mains
- Walk Transect
- Point Count Locations



Project Title:

WSD Contract No. 3/WSD/20 -
Reclaimed Water Supply to Sheung Shui and Fanling -
Provision of EM&A (Ecological) Monitoring

Figure Title:

Transect and Point Count Locations (zoomed in)

Drawn by:	JH	Scale:	1:6,000	on A3
Checked By:	NT	Date:	11 Mar 2022	
Approved by:	IV			
Figure Number:	Figure 1a			Revision: 1
