

ENVIRONMENTAL MONITORING AND AUDIT REPORT

FOR

CONTRACT No. CV/2004/02

RECONSTRUCTION OF WONG SHEK AND KO LAU WAN PUBLIC PIERS

APRIL 2005

Report No.: ET 12520

Certified by:  Date: 11-5-05  
Mr. Wilson Fok  
Environmental Specialist

Verified by:  Date: 10/5/05  
Mr. Joseph Poon  
Independent Checker (Environment)

## CONTENTS

	<u>Page</u>
<b>EXECUTIVE SUMMARY</b>	1
<b>1. INTRODUCTION</b>	
1.1 Background	3
1.2 Report Structure	3
<b>2. PROJECT INFORMATION</b>	
2.1 Site Description	3
2.2 Project Organization	4
2.3 Construction Programme	4
<b>3. ENVIRONMENTAL PERMITS AND LICENSES</b>	4
<b>4. SUMMARY OF EM&amp;A REQUIREMENTS</b>	
4.1 Monitoring Locations	5
4.2 Monitoring Parameters	5
4.3 Monitoring Frequency	5
4.4 Monitoring Equipment	6
4.5 Monitoring Equipment Calibration Requirements	7
4.6 Monitoring Methodology	7
4.7 Action and Limit Levels	7
4.8 Event and Action Plans	8
<b>5. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES</b>	8
<b>6. MONITORING RESULTS</b>	
6.1 Completed Monitoring Works	9
6.2 Water Quality Monitoring	9
<b>7. AUDIT REPORT</b>	
7.1 Water Quality Monitoring	10
7.2 Site Inspections	10
<b>8. WASTE MANAGEMENT</b>	10
<b>9. COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS</b>	11
<b>10. FUTURE KEY ISSUES</b>	11
<b>11. CONCLUSION</b>	11

### **LIST OF FIGURES**

4.1	Water Quality Monitoring Stations (Wong Shek)
4.2	Water Quality Monitoring Stations (Ko Lau Wan)
6.1	Surface and Middle Average Dissolved Oxygen - Mid-flood (Wong Shek)
6.2	Bottom Averaged Dissolved Oxygen - Mid-flood (Wong Shek)

## **LIST OF FIGURES**

- 6.3 Depth Averaged Turbidity - Mid-flood (Wong Shek)
- 6.4 Depth Averaged Suspended Solids - Mid-flood (Wong Shek)
- 6.5 Surface and Middle Average Dissolved Oxygen - Mid-ebb (Wong Shek)
- 6.6 Bottom Averaged Dissolved Oxygen - Mid-ebb (Wong Shek)
- 6.7 Depth Averaged Turbidity - Mid-ebb (Wong Shek)
- 6.8 Depth Averaged Suspended Solids - Mid-ebb (Wong Shek)
- 6.9 Surface and Middle Average Dissolved Oxygen - Mid-flood (Ko Lau Wan)
- 6.10 Bottom Averaged Dissolved Oxygen - Mid-flood (Ko Lau Wan)
- 6.11 Depth Averaged Turbidity - Mid-flood (Ko Lau Wan)
- 6.12 Depth Averaged Suspended Solids - Mid-flood (Ko Lau Wan)
- 6.13 Surface and Middle Average Dissolved Oxygen - Mid-ebb (Ko Lau Wan)
- 6.14 Bottom Averaged Dissolved Oxygen - Mid-ebb (Ko Lau Wan)
- 6.15 Depth Averaged Turbidity - Mid-ebb (Ko Lau Wan)
- 6.16 Depth Averaged Suspended Solids - Mid-ebb (Ko Lau Wan)

## **TABLES**

- Table 3.1 Summary of the Environmental Permits and Licenses
- Table 4.1 Coordinates of Water Quality Monitoring Locations
- Table 4.2 Action and Limit Levels for Water Quality Monitoring
- Table 6.1 Completed Monitoring Works for April 2005
- Table 6.2 Summary of Water Quality Monitoring Data
- Table 10.1 Works Programme for May 2005

## **APPENDICES**

- I Organization Chart
- II Calibration Certificates of the Monitoring Equipment
- III Event and Action Plans
- IV Implementation Status of Mitigation measures
- V Water Quality Monitoring Results
- VI Complaint Log
- VII Cumulative Statistics on Complaints, Notifications of Summonses and Successful Prosecutions
- VIII Monitoring Schedule for the Next Month
- IX Master Construction Programme

## EXECUTIVE SUMMARY

This is the 2<sup>nd</sup> monthly Environmental Monitoring and Audit (EM&A) report for Contract No. CV/2004/02 – Reconstruction of Wong Shek and Ko Lau Wan Public Piers and it covers the environmental monitoring works conducted in April 2005.

### Construction Activities for the Reported Period

Major construction works carried out this month included:

#### *Wong Shek*

- Ground Investigation
- Installation of silt curtain
- Piling work for temporary berth

#### *Ko Lau Wan*

- Ground Investigation
- Coral survey and translocation

### Water Quality Monitoring

Water quality monitoring in terms of turbidity, dissolved oxygen, suspended solids, temperature, and salinity was carried out on ten occasions at MW1, MW2, CW1 and CW2 at Wong Shek Pier and three occasions at MK1, MK2, MK3, MK4, CK1 and CK2 at Ko Lau Wan Pier. There were no exceedances to set Action Levels and Limit Levels for all parameters recorded during the reported period.

### Waste Management

No C&D material, general refuse or chemical waste was transported off site in this reported period.

### Complaints, Notifications of Summons and Successful Prosecutions

No complaints, notifications of summons and successful prosecutions were received this month.

### Site Inspections

Four site inspections were conducted by Environmental Specialist (ES) in this reported period. Major observations by the ET, outcome are summarized in the following table

Observations by ET	Environmental Outcome
Coral Exclusion Zone mark was removed by the sea wave	Buoys mark the Coral Exclusion Zone have been mount by the contractor
Little diesel oil was found floating on the sea surface near the Wong Shek pier.	Unidentified source of Diesel oil was observed but it was not generated from the construction works.
Environmental Permit was not displayed at the site entrance	Environmental Permit has been displayed at the site entrance by the contractor



### Future Key Issues

The tentative works activities, predicted impacts and areas of environmental concern for the month following this reported period are summarized in the following table.

Works Activities	Predicted Impacts	Proposed Mitigation Measures
Ground Investigation	<ul style="list-style-type: none"><li>· Water</li><li>· Air</li></ul>	<ul style="list-style-type: none"><li>· The flushing water should be reused as much as possible and the effluent should be treated to acceptable quality before discharge.</li><li>· The rig should be maintain in good condition to avoid emitting excessive black smoke.</li></ul>
Piling work for temporary berth.	<ul style="list-style-type: none"><li>· Water</li></ul>	<ul style="list-style-type: none"><li>· The silt curtain should be properly installed before carrying out the piling work.</li></ul>
Erection of deck for temporary berth	<ul style="list-style-type: none"><li>· Noise</li><li>· Waste</li></ul>	<ul style="list-style-type: none"><li>· Avoid concurrent noisy operation during the erection of deck for the temporary berth</li><li>· Construction and demolition materials should be sorted</li></ul>

### Reporting of Changes

Generally, the baseline monitoring was conducted according to the Particular Specification (PS) Section 26 - Environmental Mitigation Measures and Monitoring Requirements and hence no revision to the EM&A requirements was made.

## **1. INTRODUCTION**

### **1.1 Background**

Stanger Asia Ltd. has been commissioned by Kin Shing Construction Company Limited to provide an Environmental Specialist (ES) to carry out the environmental monitoring and audit works for the Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers. The team is to take a pro-active role in all issues, which may be of environmental concern during the construction period of the Project.

In this report, the water quality monitoring works conducted in April 2005 will be detailed and reviewed. This report has been produced with reference to the Section 26 of the Particular Specification, Project Profile (PP-191/2003) and Environmental Permit (EP-186/2004) produced for this Project.

### **1.2 Report Structure**

The purpose of this report is to detail and review the water quality monitoring works undertaken for April 2005. The impact forecast for the next reporting month and the schedules of monitoring works for the following month are also given.

The report follows the format given below:

Section 1:	Introduction and background information to the content of this report
Section 2:	This section gives the information of the project
Section 3:	This section summarizes all the environmental permits and licenses
Section 4:	Summary of the EM&A requirements is presented
Section 5:	This section details the implemented mitigation measures
Section 6:	Details monitoring results
Section 7:	Audit the monitoring results
Section 8:	The status for solid and liquid waste management for the site is overviewed
Section 9:	Complaints, notifications of summons and successful prosecutions are summarized
Section 10:	This section gives the predicted impacts of the construction activities
Section 11:	This section gives a conclusion in relation to all monitoring activities.

## **2. PROJECT INFORMATION**

### **2.1 Site Description**

The construction works, Contract No. CV/2004/02, is to be carried out under the direction of the Civil Engineering Office, Civil Engineering and Development Department. It comprises demolition of the existing piers and construction of reinforced concrete piers with roof covers at Wong Shek and Ko Lau Wan.

The construction of the Project is scheduled to commence in November 2004 for completion in August 2006. The construction period is 630 days for the entire construction.

## 2.2 Project Organization

The Project Proponent and the Engineer is Civil Engineering Office, Civil Engineering and Development Department. The Resident Engineer is Mr. W H Lee.  
(Tel: 2760 5737; Fax: 2714 2054; Mobile Phone No: 9630 1235)

The Main Contractor for this project is Kin Shing Construction Company Limited. The Site Agent is Mr. Simon Fok  
(Tel: 2729 6779; Fax: 2729 7858; Mobile Phone No: 6010 8730).

The Independent Checker (Environment) is MaterialLab Consultants Limited. The Manager is Mr. Joseph T L Poon.  
(Tel: 2452 7140; Fax: 2450 6138; Mobile Phone No: 9450 1968)

The Environmental Specialist proposed for this project is Stanger Asia Limited. The Environmental Specialist is Mr. Wilson Fok.  
(Tel: 2682 1203; Fax: 2682 0046; Mobile Phone No: 6105 4260)  
The environmental organization chart is attached in Appendix I

## 2.3 Construction Programme

Details of the construction activities carried out in April 2005 are summarized below. The master construction programme is given in Appendix IX.

*Wong Shek*

- Ground Investigation
- Installation of silt curtain
- Piling work for temporary berth

*Ko Lau Wan*

- Ground Investigation
- Coral survey and translocation

## 3. ENVIRONMENTAL PERMITS AND LICENSES

The summary of the status of all environmental permits, licenses and notification for this project as of April 2005 is summarized in the following table.

**Table 3.1 Summary of the Environmental Permits and Licenses**

Description	Licence/ Permit No.	Issued Date	Expiry Date	Status
Environmental Permit	EP-186/2004	16 Mar 04	--	Issued

## 4. SUMMARY OF EM&A REQUIREMENTS

### 4.1 Monitoring Locations

For Wong Shek, MW1 and MW2 are the two designated monitoring stations whereas CW1 and CW2 are the two designated control stations. For Ko Lau Wan, MK1 to MK4 are the four designated monitoring stations whereas CK1 and CK2 are the two designated control stations. CW1 and CK2 are the control stations during flood tides whereas CW2 and CK1 are the control stations during ebb tides.

The locations of each station are given Figure 4.1 and Figure 4.2, their coordinates are given in Table 4.1 below.

**Table 4.1 Coordinates of Water Quality Monitoring Locations**

Station	HK Metric Grid – Easting	HK Metric Grid - Northing
<b><i>Wong Shek Public Pier</i></b>		
MW1	852 789.231	832 978.476
MW2	852 844.187	832 878.676
CW1	852 922.540	833 067.718
CW2	852 992.314	832 853.794
<b><i>Ko Lau Wan Public Pier</i></b>		
MK1	855 212.850	835 496.101
MK2	855 158.643	835 539.315
MK3	855 170.762	835 401.962
MK4	855 108.767	835 402.196
CK1	854 822.145	835 428.000
CK2	854 996.976	835 675.135

### 4.2 Monitoring Parameters

Water quality shall be monitored in terms of: dissolved oxygen (mg/L and % saturation), salinity (ppt), turbidity (NTU), and suspended solids (mg/L).

The parameters of dissolved oxygen, salinity and turbidity were measured on-site with portable instruments. Other relevant data was also recorded, including monitoring location / position, time, water depth, salinity, temperature, tidal stages, weather conditions and any special phenomena or work underway at the construction site.

The measurement of suspended solids was carried out in the laboratory of Stanger Asia Ltd. within 24 hours of sampling. The laboratory is HOKLAS accredited to determine suspended solids content in accordance with APHA Method No. 2540D, 20<sup>th</sup> Edition.

### 4.3 Monitoring Frequency

*Impact Monitoring – piling and demolition works*

Monitoring shall be undertaken three days per week, at mid-flood and mid-ebb. The interval between two sets of monitoring shall not be less than 36 hours except where there are exceedances of Action and /or Limit levels, in which case the monitoring frequency shall be increased.

*Impact Monitoring – marine works other than piling and demolition works*

Monitoring shall be undertaken one day per week, at mid-flood and mid-ebb. The interval between two sets of monitoring shall not be less than 36 hours except where there are exceedances of Action and /or Limit levels, in which case the monitoring frequency shall be increased.

#### **4.4 Monitoring Equipment**

Monitoring of marine water quality shall be carried out employing the following equipment.

*Dissolved Oxygen, Salinity and Temperature Measuring Equipment*

A YSI model 85 Handheld Dissolved Oxygen, Conductivity, Salinity and Temperature System was employed.

The instrument is portable, weatherproof instrument complete with cable, sensor, comprehensive operation manuals and operates from a DC power source. It is capable of measuring:

- (a) dissolved oxygen in the range of 0-20mg/L and 0-200% saturation
- (b) temperature in the range of 5 - 65°C
- (c) salinity in the range of 0-80ppt

The instrument has a membrane electrode with automatic temperature and salinity compensation, complete with a cable of sufficient length. Sufficient stocks of spare electrodes and cables are available for replacement where necessary.

*Turbidity Measurement Instrument*

A Hach 2100P turbidimeter shall be employed

This instrument measures turbidity on-site by the nephelometric method. The instrument is portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment operates from a DC power source and has a photoelectric sensor capable of measuring turbidity between 0-1000NTU.

*Suspended Solids*

A Kahlisco Water Sampler 135WB203 was employed. This is a “Van Dorn” type of sampler, which has a transparent PVC cylinder (of a capacity not less than 2 litres) and can be effectively sealed with cups at both ends, shall be used for sampling. The sampler has a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is to the selected water depth.

Water samples for suspended solids measurements shall be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to the laboratory as soon as possible after collection.

### *Water Depth*

A Hummingbird 100SX digital echo-sounder was employed. This is a portable, battery-operated Echo Sounder to be used for the determination of water depth at each water quality monitoring and control station. This unit can be either be hand-held or affixed to the bottom of the work boat if the same vessel is used throughout the monitoring programme.

### *Vessel Positioning Device*

A Trimble NT200D Differential Global Positioning (DGPS) was employed. This is a portable or boat fixed and has an accuracy of  $\pm 1\text{m}$  and can be programmed with waypoints to ensure the correct and repeated positioning of a vessel at a given monitoring location.

## **4.5 Monitoring Equipment Calibration Requirements**

All on-site monitoring equipment shall be checked, verified and calibrated by Stanger Asia Limited, a HOKLAS accredited laboratory, prior to use on the Works and subsequently thereafter every three months throughout all stages of the water quality monitoring. Responses of the sensors and electrodes shall be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement.

For on-site calibration of field equipment, the BS 1427: 1993 “Guide to Field and on-site test methods for the analysis of waters” shall be observed.

A set of backup monitoring instruments and equipment shall be made available so that the monitoring can proceed uninterrupted in case of apparatus malfunction or if equipment has been returned to the laboratory for calibration.

## **4.6 Monitoring Methodology**

Measurements were be taken under two tidal conditions (mid-flood and mid-ebb) at 3 water depths, namely 1m below the water surface, mid-depth and 1m above the seabed, except where the water depth is less than 6m, the mid-depth sample may be omitted. If the water depth is less than 3m, only the mid-depth will be monitored.

Replicate in-situ measurements and samples were collected from each independent sampling event are required for all parameters to ensure a robust statistical interpretable dataset.

For the measurement of dissolved oxygen the probe shall be removed from the water column between each duplicate measurement. If the difference between each duplicate measurement is greater than a 25% then the two sets of data shall be rejected and the measurements re-taken.

## **4.7 Action and Limit Levels**

Water quality criteria, namely Action and Limit levels were based on the results of the baseline monitoring programme. The Action and Limit levels were calculated according to the following table.

**Table 4.2 Action and Limit Levels for Water Quality Monitoring**

Parameter	Action Level	Limit Level
Dissolved Oxygen in mg/L (Surface, Middle & Bottom)	<u>Surface &amp; Middle</u> For Wong Shek - 6.96  For Ko Lau Wan - 6.90	<u>Surface &amp; Middle</u> For Wong Shek - 6.69  For Ko Lau Wan - 6.79
	<u>Bottom</u> For Wong Shek - 6.93  For Ko Lau Wan - 6.75	<u>Bottom</u> For Wong Shek - 6.71  For Ko Lau Wan - 5.63
SS in mg/L (depth-averaged)	For Wong Shek - 6.85 or 120% of upstream control station's SS at the same tide of same day, whichever is lower  For Ko Lau Wan - 6.30 or 120% of upstream control station's SS at the same tide of same day, whichever is lower	For Wong Shek - 8.85 or 130% of upstream control station's SS at the same tide of same day, whichever is lower  For Ko Lau Wan - 6.87 or 130% of upstream control station's SS at the same tide of same day, whichever is lower
Turbidity (Tby) in NTU (depth-averaged)	For Wong Shek - 1.47 or 120% of upstream control station's Tby at the same tide of same day, whichever is lower  For Ko Lau Wan - 1.25 or 120% of upstream control station's Tby at the same tide of same day, whichever is lower	For Wong Shek - 4.05 or 130% of upstream control station's Tby at the same tide of same day, whichever is lower  For Ko Lau Wan - 1.60 or 130% of upstream control station's Tby at the same tide of same day, whichever is lower

- Notes: (a) "depth-averaged" is calculated by taking the arithmetic means of reading all three depths.  
 (b) For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.  
 (c) For SS and Tby, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.  
 (d) All the figures given in the table are used for reference only and the Engineer may amend the figures whenever it is considered as necessary.

#### **4.8 Event and Action Plans**

The Event and Action Plans for air, noise and water are attached in Appendix III of this report.

#### **5. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES**

The contractor implemented various environmental mitigation measures as recommended in the Particular Specification and Environmental Permit. The implementation status is attached in Appendix IV.

## 6. MONITORING RESULTS

### 6.1 Completed Monitoring Works

Table 6.1 gives the completed monitoring works for the reported period.

**Table 6.1 Completed Monitoring Works for April 2005**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1	2
3	4 WQM <sup>1</sup> (Ebb: 09:17) (Flood: 13:46)		6 WQM <sup>3</sup> (Ebb: 10:43) (Flood: 16:22)	7	8 WQM <sup>1</sup> (Ebb: 12:10) (Flood: 18:13)	9
10	11 WQM <sup>1</sup> (Ebb: 14:08) (Flood: 07:47)	12	13	14	15	16
17	18	19 WQM <sup>3</sup> (Ebb: 09:24) (Flood: 13:28)	20	21 WQM <sup>1</sup> (Ebb: 10:51) (Flood: 16:27)	22	23 WQM <sup>1</sup> (Ebb: 11:53) (Flood: 18:05)
24	25 WQM <sup>1</sup> (Ebb: 13:06) (Flood: 06:44)	26	27 WQM <sup>3</sup> (Ebb: 13:02) (Flood: 06:14)	28	29 WQM <sup>1</sup> (Ebb: 14:37) (Flood: 07:00)	30

Notes: 1. WQM - water quality monitoring on mid-flood and mid-ebb tides at Wong Shek (CW1, CW2, MW1 & MW2)  
 2. WQM - water quality monitoring on mid-flood and mid-ebb tides at Ko Lau Wan (CK1, CK2, MK1, MK2, MK3 & MK4)  
 3. WQM - water quality monitoring on mid-flood and mid-ebb tides at Ko Lau (CK1, CK2, MK1, MK2, MK3 & MK4) and Wong Shek (CW1, CW2, MW1 & MW2)

### 6.2 Water Quality Monitoring

Water quality monitoring in terms of turbidity, dissolved oxygen, suspended solids, temperature, and salinity was carried out on ten occasions at MW1, MW2, CW1 and CW2 at Wong Shek Pier and three occasions at MK1, MK2, MK3, MK4, CK1 and CK2 at Ko Lau Wan Pier. Results for water quality monitoring are summarised in the following table. Detailed monitoring results are presented in Appendix V. Graphical presentations of the results are shown in Figure 6.1 – Figure 6.16.

**Table 6.2 Summary of Water Quality Monitoring Data**

Sample Location	Surface & Middle Averaged DO, mg/L	Bottom Averaged DO, mg/L	Averaged Turbidity, NTU	Averaged Suspended Solids, mg/L
Wong Shek - Flood Tide				
MW1	7.34	7.34	0.76	4.7
MW2	7.50	7.36	0.78	4.7
CW1	7.23	7.22	0.81	5.1
CW2	7.48	7.31	0.81	5.3
Wong Shek- Ebb Tide				
MW1	7.34	7.34	0.77	5.1
MW2	7.35	7.31	0.77	5.1
CW1	7.15	7.33	0.80	5.3
CW2	7.44	7.29	0.81	5.4



**Table 6.2 Summary of Water Quality Monitoring Data (continued)**

Sample Location	Surface & Middle Averaged DO, mg/L	Bottom Averaged DO, mg/L	Averaged Turbidity, NTU	Averaged Suspended Solids, mg/L
Ko Lau Wan - Flood Tide				
MK1	7.22	6.91	0.63	4.3
MK2	7.24	7.02	0.68	4.6
MK3	7.27	6.90	0.67	5.0
MK4	7.17	7.04	0.60	5.0
CK1	7.40	6.91	0.65	5.1
CK2	7.21	6.87	0.66	5.1
Ko Lau Kan - Ebb Tide				
MK1	7.13	7.17	0.66	4.2
MK2	7.32	6.74	0.72	4.5
MK3	7.28	7.22	0.66	4.5
MK4	7.21	6.93	0.66	4.7
CK1	7.45	7.03	0.64	4.6
CK2	7.55	6.78	0.71	4.8

## 7. AUDIT REPORT

### 7.1 Water Quality Monitoring

There were no exceedances to Trigger, Action and Target Level for any parameters in this reported period.

### 7.2 Site Inspections

Four site inspections were conducted by Environmental Specialist (ES) in this reported period. Major observations by the ET, outcome are summarized in the following table

Observations by ET	Environmental Outcome
Coral Exclusion Zone mark was removed by the sea wave	Buoys mark the Coral Exclusion Zone have been mount by the contractor
Little diesel oil was found floating on the sea surface near the Wong Shek pier.	Unidentified source of Diesel oil was not generated from the construction works.
Environmental Permit was not displayed at the site entrance	Environmental Permit has been displayed at the site entrance by the contractor

## 8. WASTE MANAGEMENT

No C&D material, general refuse or chemical waste was transported off site in this reported period.

**9. COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS**

No complaints, notifications of summons and successful prosecutions were received.

Complaint Log is attached in Appendix VI. Cumulative statistics on complaints, notifications of summons and successful prosecutions are attached in Appendix VII.

**10. FUTURE KEY ISSUES**

The following are the scheduled construction activities for the next reported period. Scheduled monitoring activities for the following month is given in Appendix VIII.

**Table 10.1 Works Programme for May 2005**

Works Activities	Predicted Impacts	Proposed Mitigation Measures
Ground Investigation	<ul style="list-style-type: none"><li>· Water</li><li>· Air</li></ul>	<ul style="list-style-type: none"><li>· The flushing water should be reused as much as possible and the effluent should be treated to acceptable quality before discharge.</li><li>· The rig should be maintain in good condition to avoid emitting excessive black smoke.</li></ul>
Piling work for temporary berth.	<ul style="list-style-type: none"><li>· Water</li></ul>	<ul style="list-style-type: none"><li>· The silt curtain should be properly installed before carrying out the piling work.</li></ul>
Erection of deck for temporary berth	<ul style="list-style-type: none"><li>· Noise</li><li>· Waste</li></ul>	<ul style="list-style-type: none"><li>· Avoid concurrent noisy operation during the erection of deck for the temporary berth</li><li>· Construction and demolition materials should be sorted</li></ul>

**11. CONCLUSION**

For water quality monitoring, there were no exceedances to set Action Level and Limit Levels recorded during the reported period.

No complaints, notifications of summons and successful prosecutions were received in this month.

## Figures

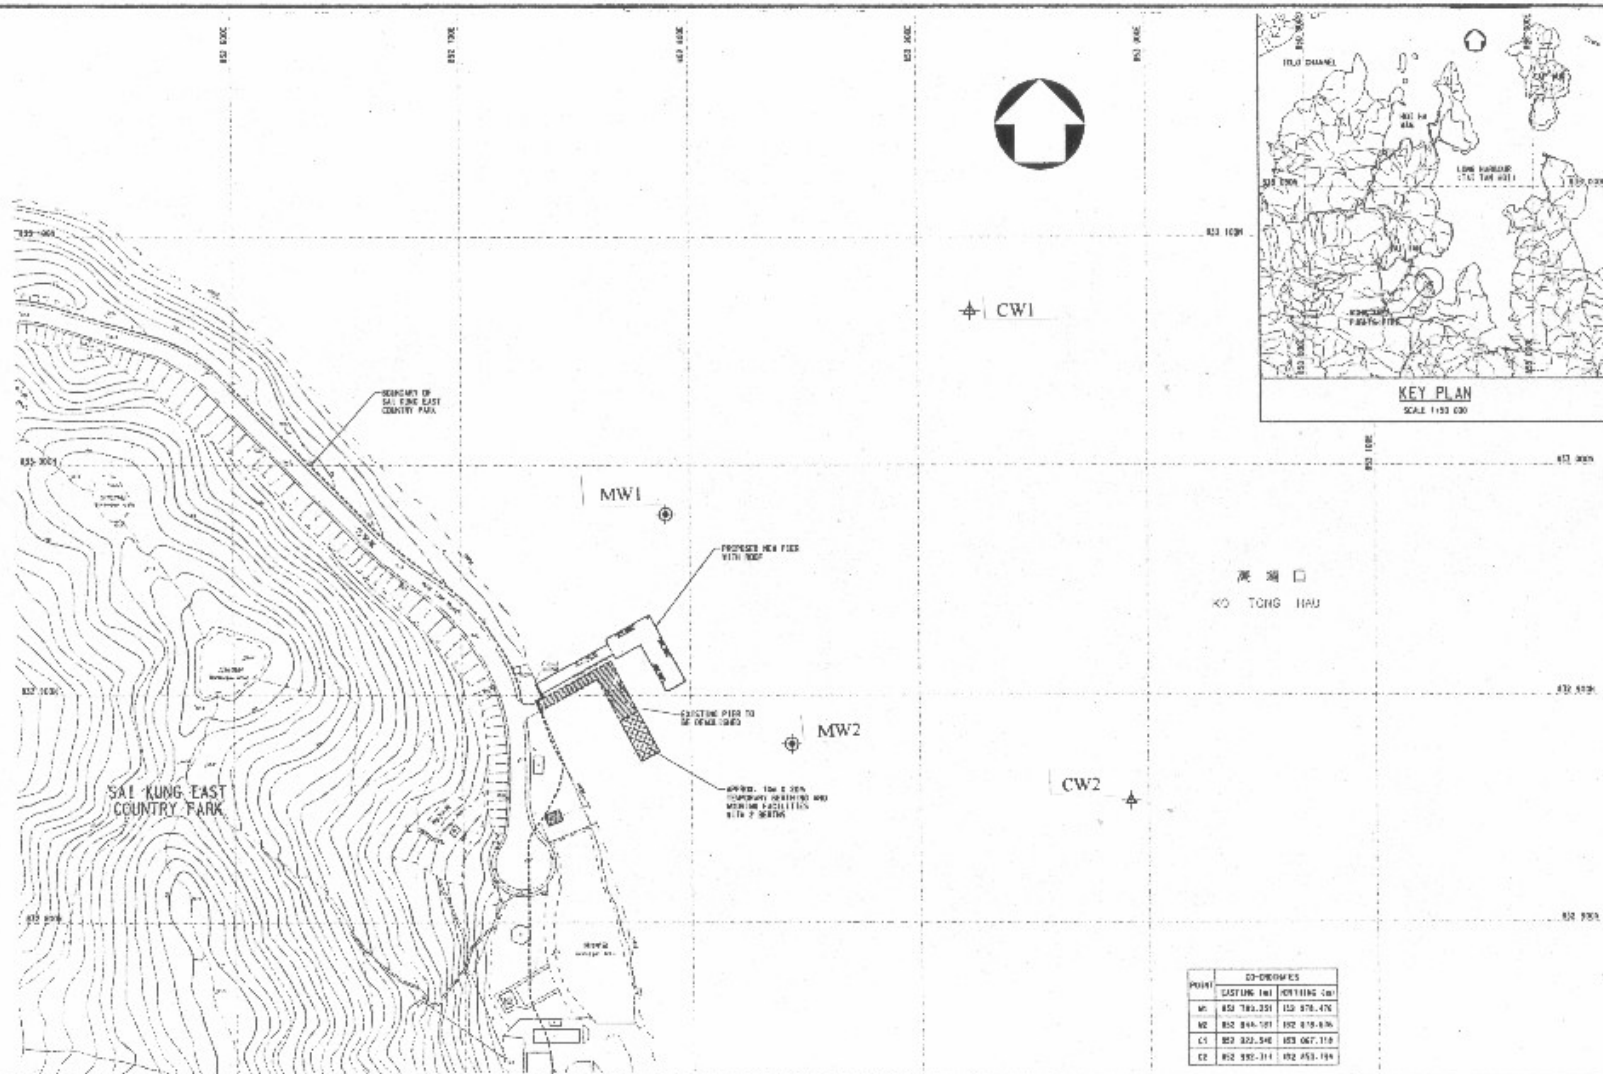


Figure 4.1 - Water Quality Monitoring Stations (Wong Shek)

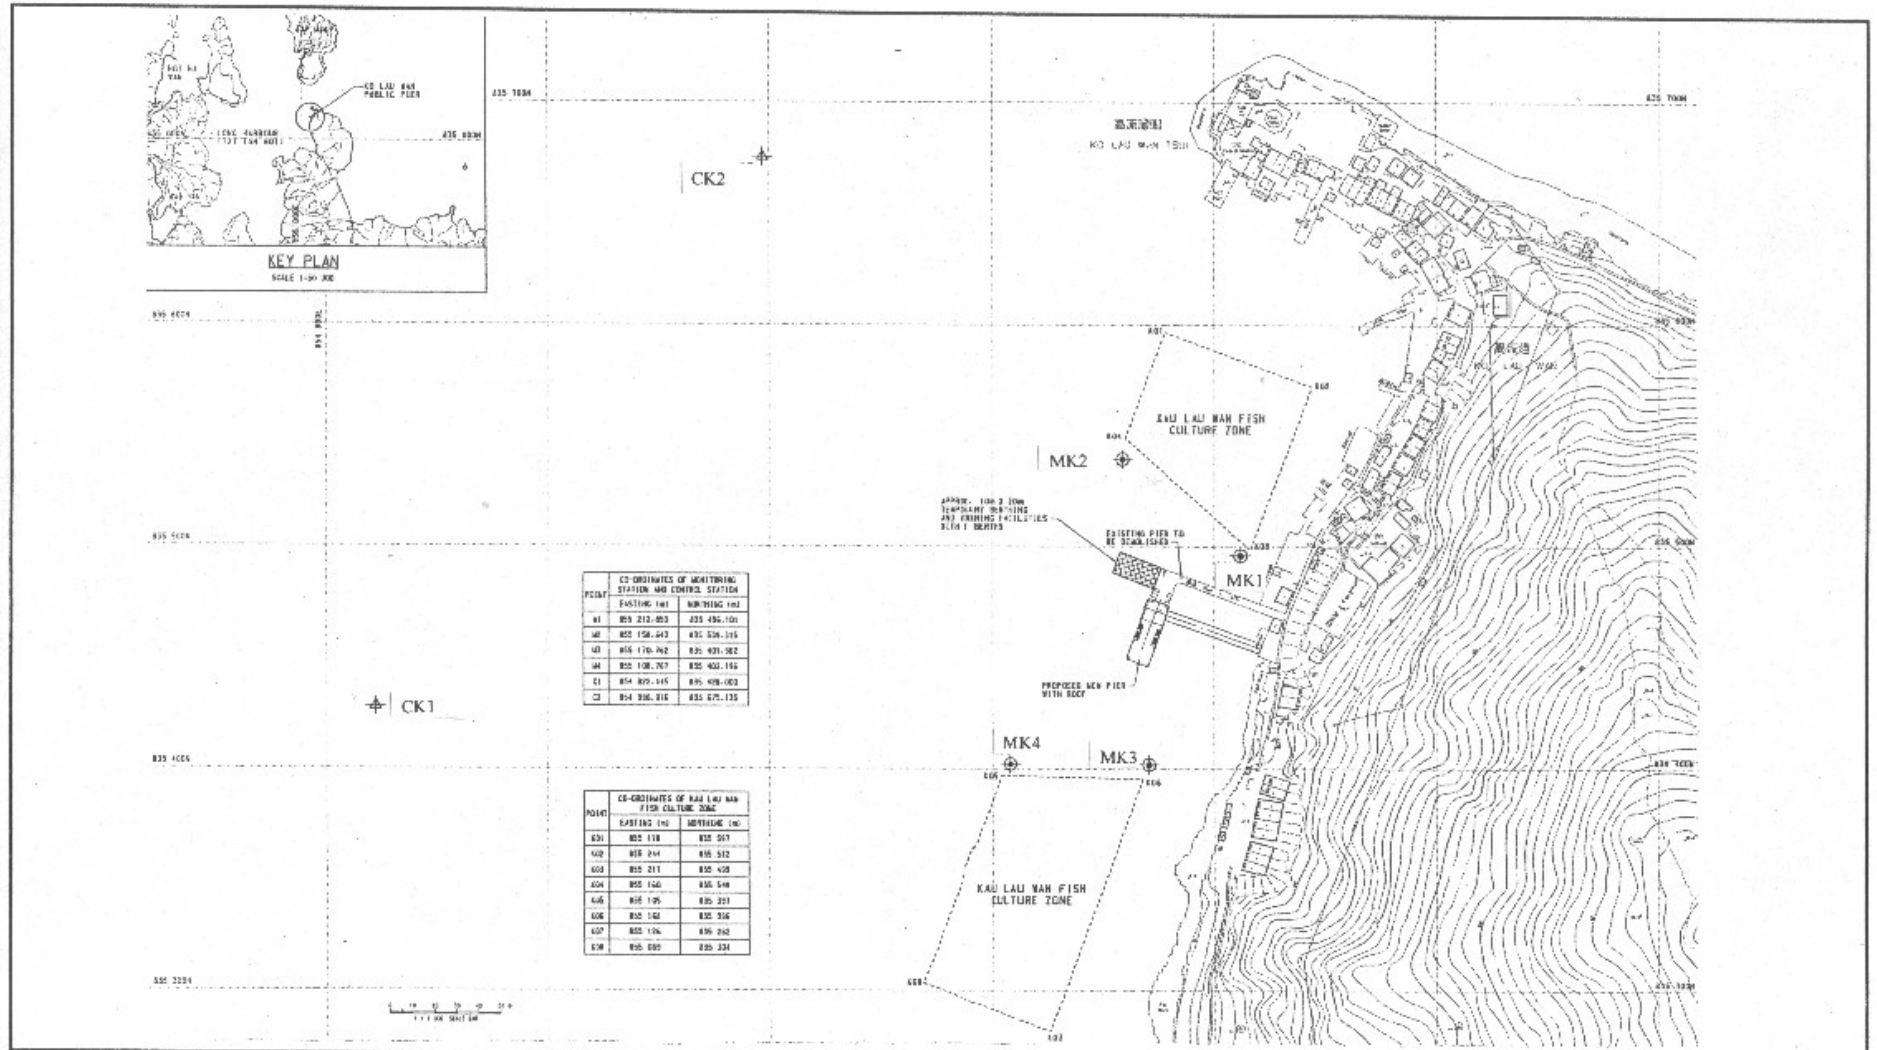
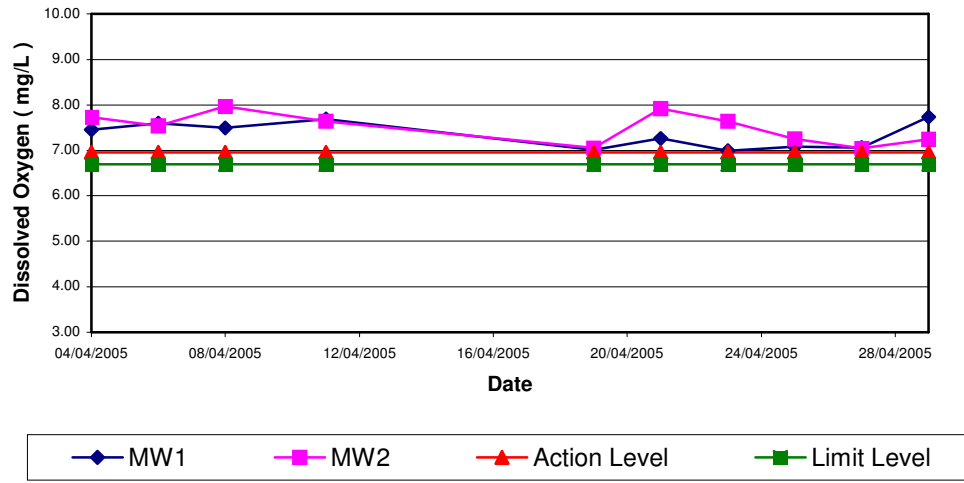


Figure 4.2 - Water Quality Monitoring Stations (Ko Lau Wan)

**Figure 6.1 - Surface and Middle Averaged Dissolved Oxygen - Mid-Flood (Wong Shek)**



**Figure 6.2 - Bottom Averaged Dissolved Oxygen - Mid-Flood (Wong Shek)**

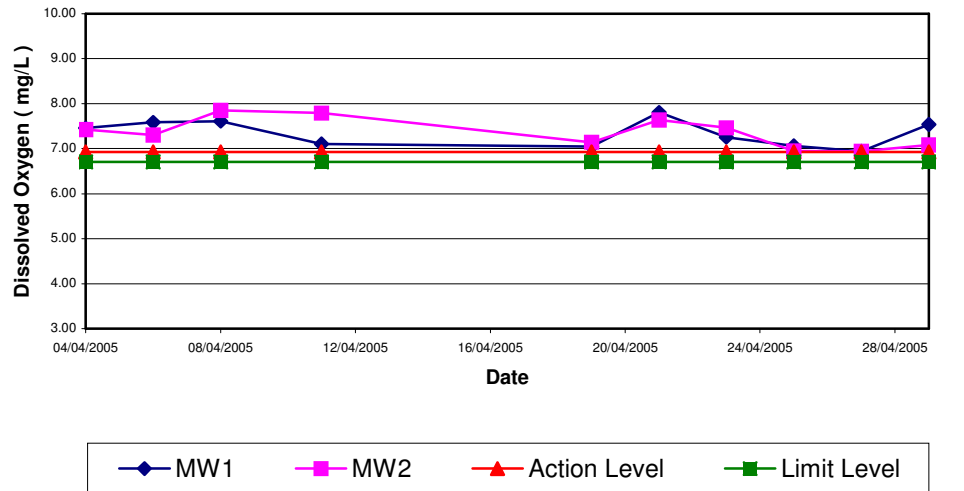


Figure 6.3 - Depth Averaged Turbidity - Mid-Flood  
(Wong Shek)

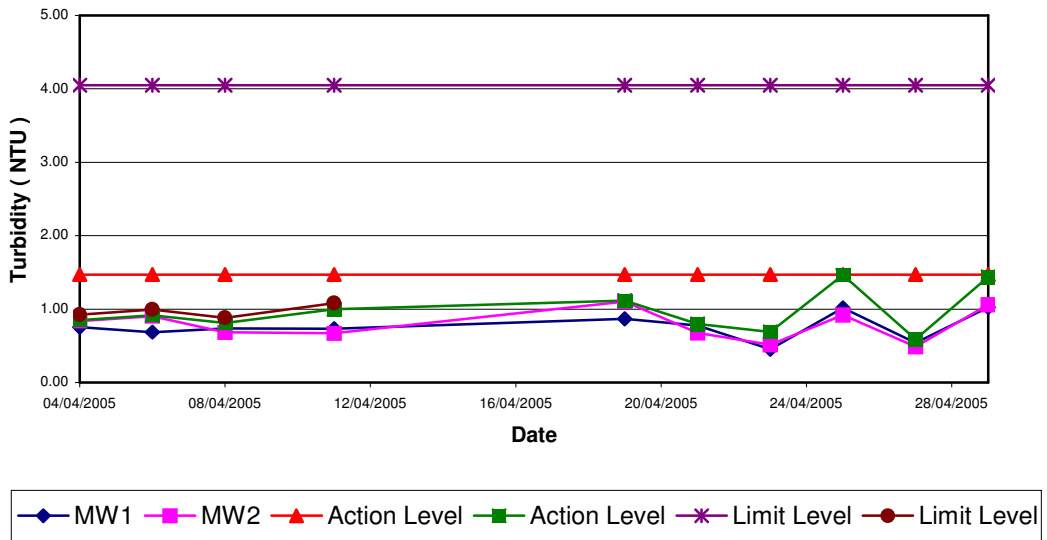
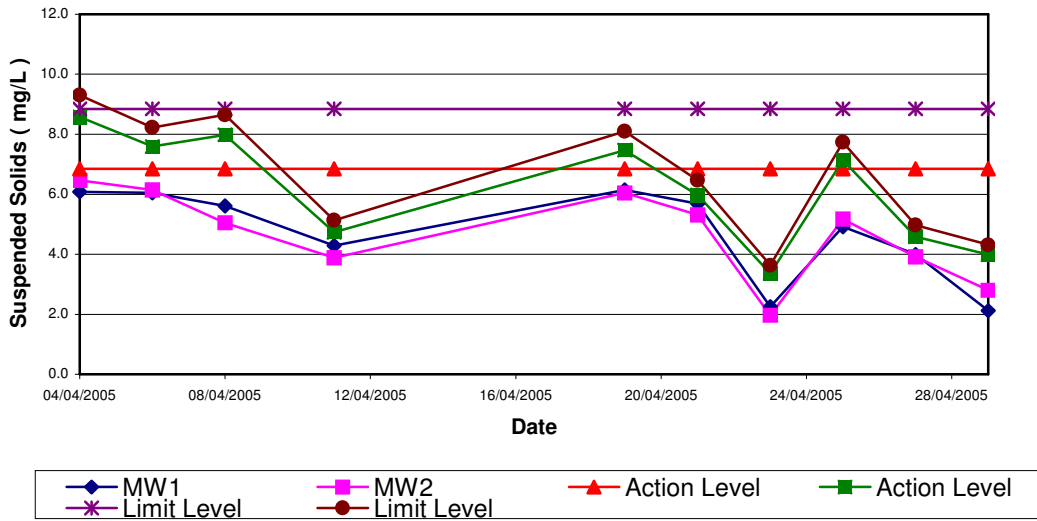
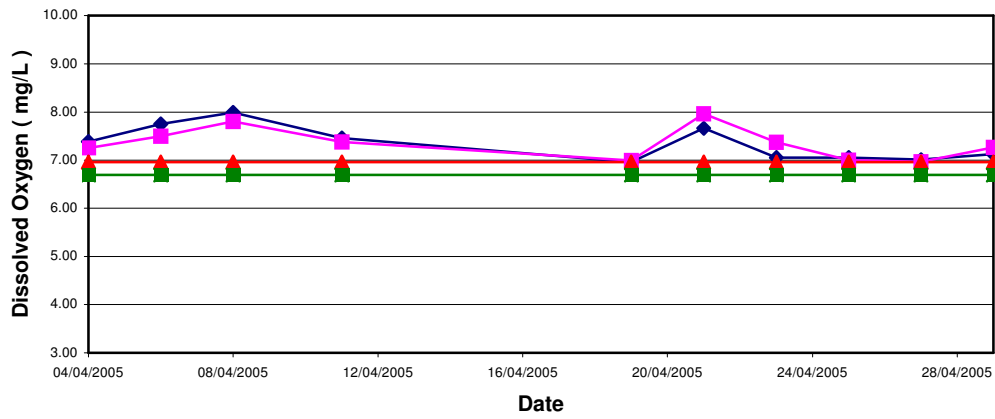


Figure 6.4 - Depth Averaged Suspended Solids - Mid-Flood  
(Wong Shek)



**Figure 6.5 - Surface and Middle Averaged Dissolved Oxygen - Mid-Ebb  
(Wong Shek)**



**Figure 6.6 - Bottom Averaged Dissolved Oxygen - Mid-Ebb  
(Wong Shek)**

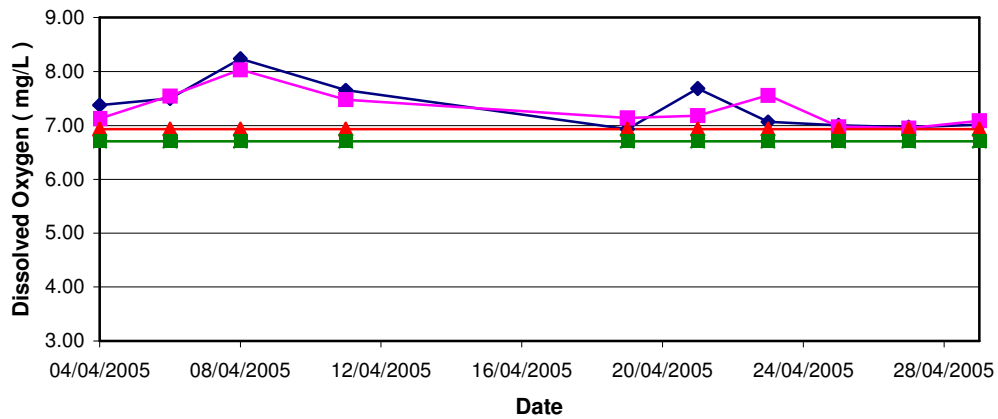




Figure 6.7 - Depth Averaged Turbidity - Mid-Ebb  
(Wong Shek)

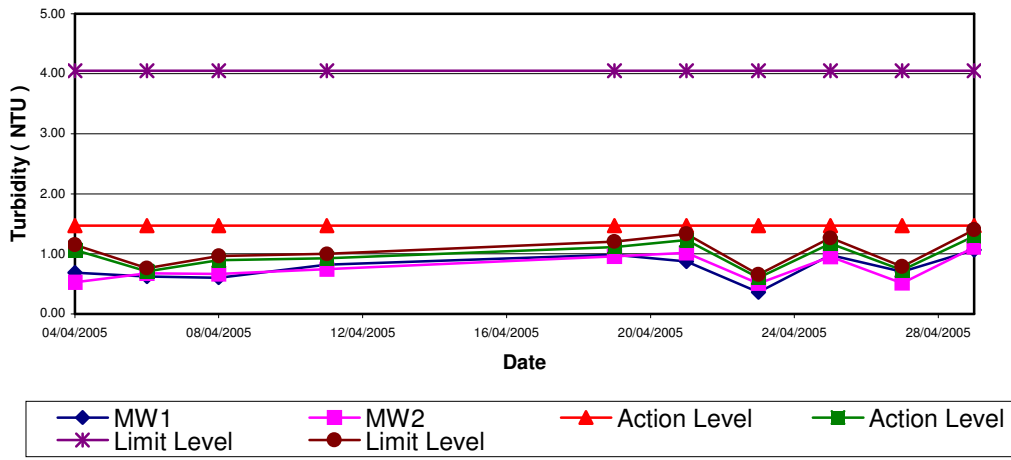
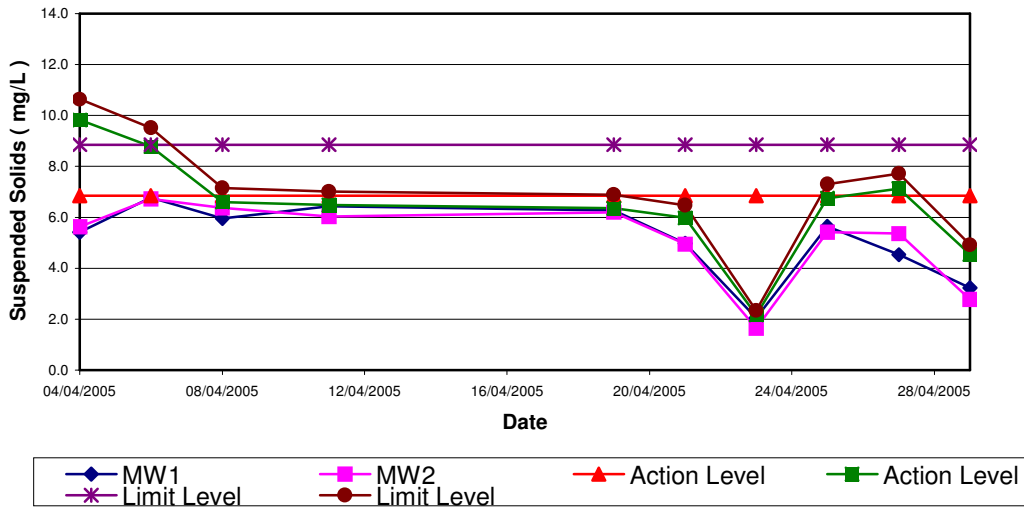
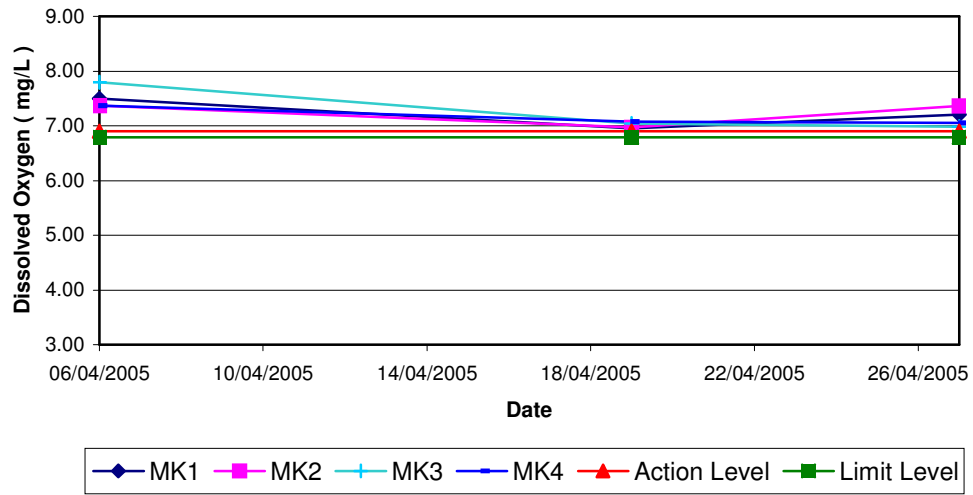


Figure 6.8 - Depth Averaged Suspended Solids - Mid-Ebb  
(Wong Shek)



**Figure 6.9 - Surface and Middle Averaged Dissolved Oxygen - Mid-Flood  
(Ko Lau Wan)**



**Figure 6.10 - Bottom Averaged Dissolved Oxygen - Mid-Flood  
(Ko Lau Wan)**

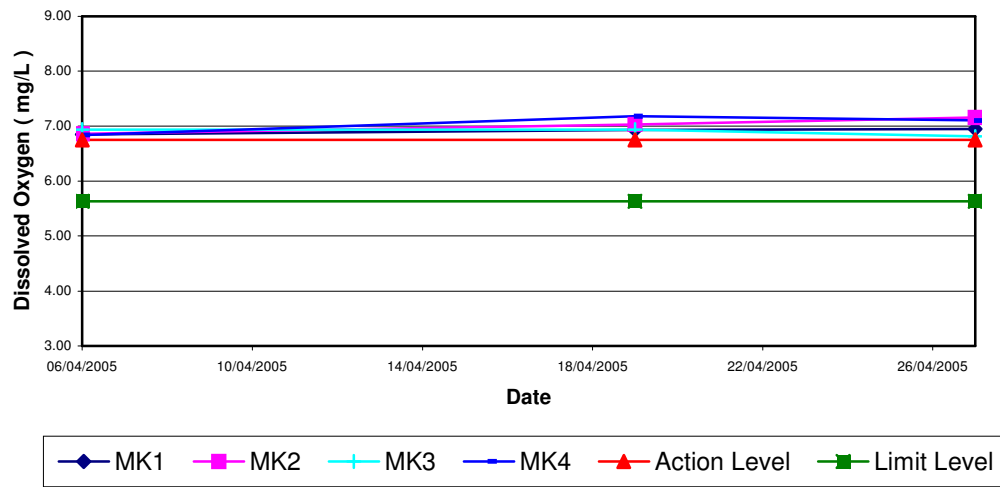


Figure 6.11 - Depth Averaged Turbidity - Mid-Flood  
(Ko Lau Wan)

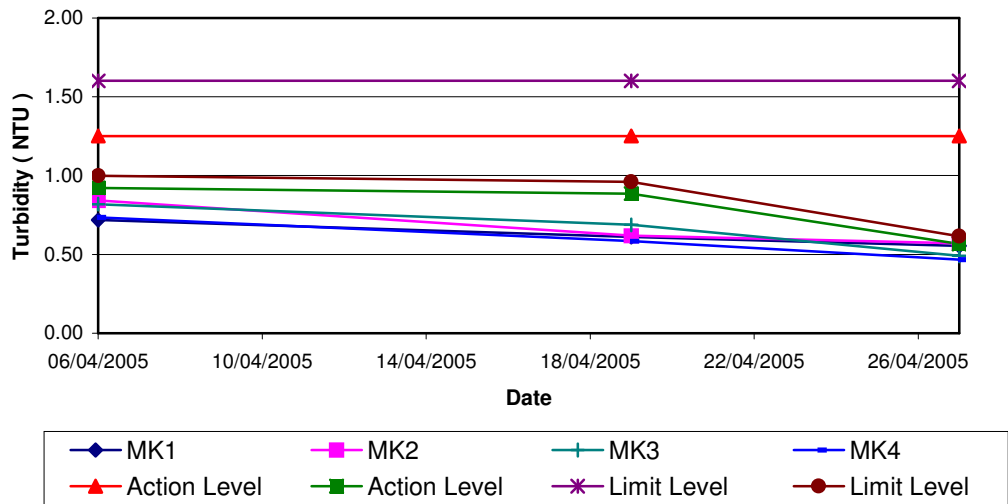


Figure 6.12 - Depth Averaged Suspended Solids - Mid-Flood  
(Ko Lau Wan)

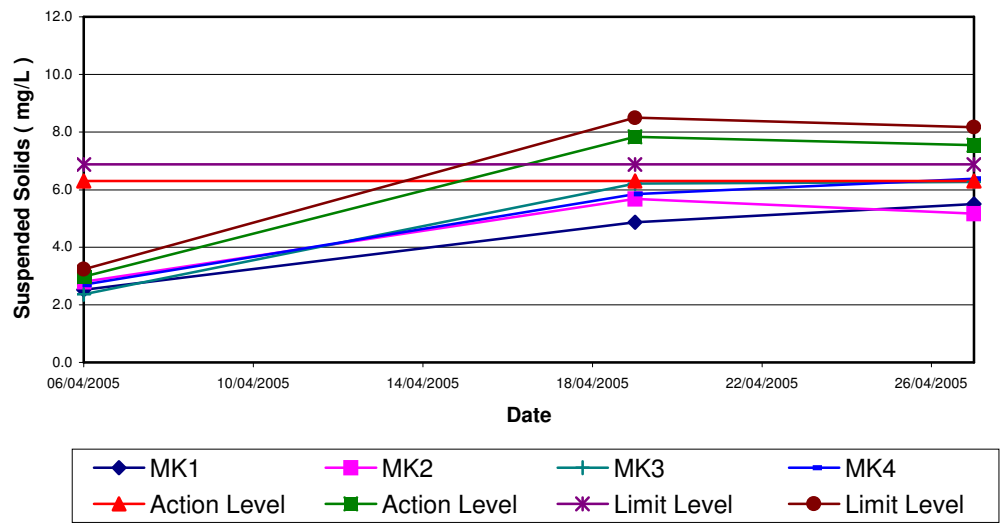


Figure 6.13 - Surface and Middle Averaged Dissolved Oxygen - Mid-Ebb  
(Ko Lau Wan)

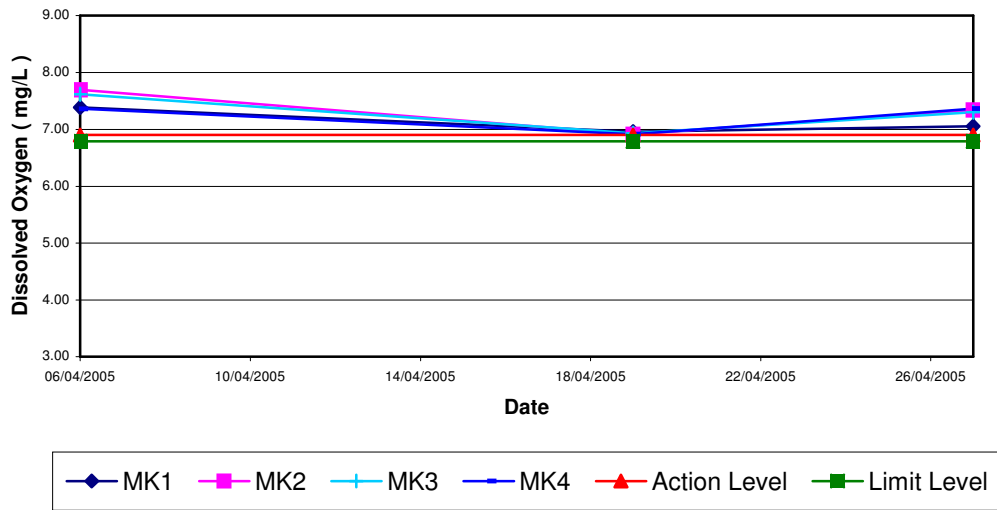


Figure 6.14 - Bottom Averaged Dissolved Oxygen - Mid-Ebb  
(Ko Lau Wan)

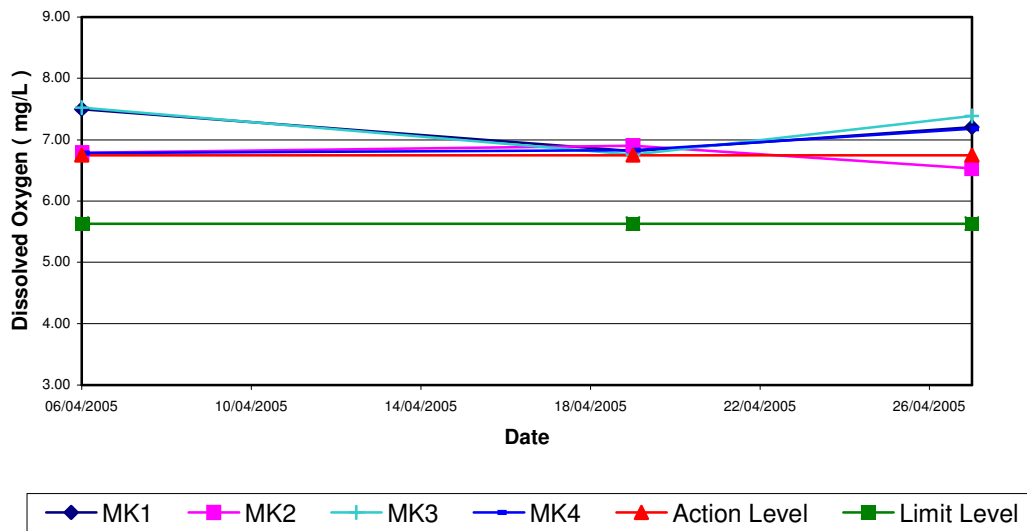


Figure 6.15 - Depth Averaged Turbidity - Mid-Ebb  
(Ko Lau Wan)



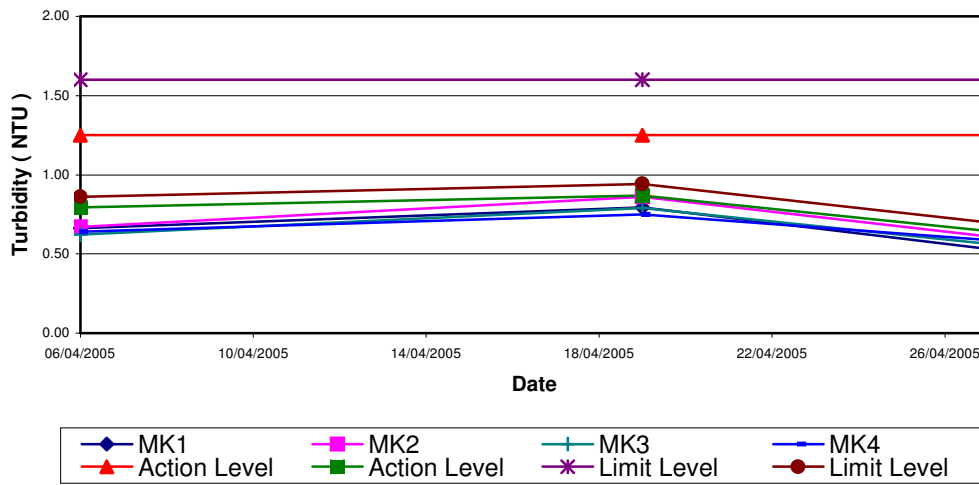


Figure 6.16 - Depth Averaged Suspended Solids - Mid-Ebb  
(Ko Lau Wan)

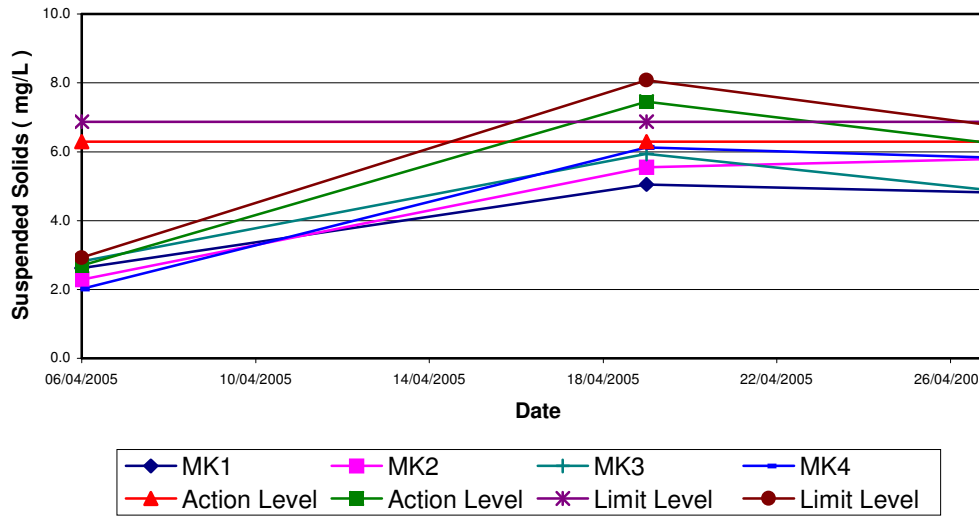

**Appendix I**  
**Organisation Chart**

**Contract No. CV/2004/02**  
**Reconstruction of Wong Shek and Ko Lau Wan Public Piers**  
**Environmental Organization Chart**

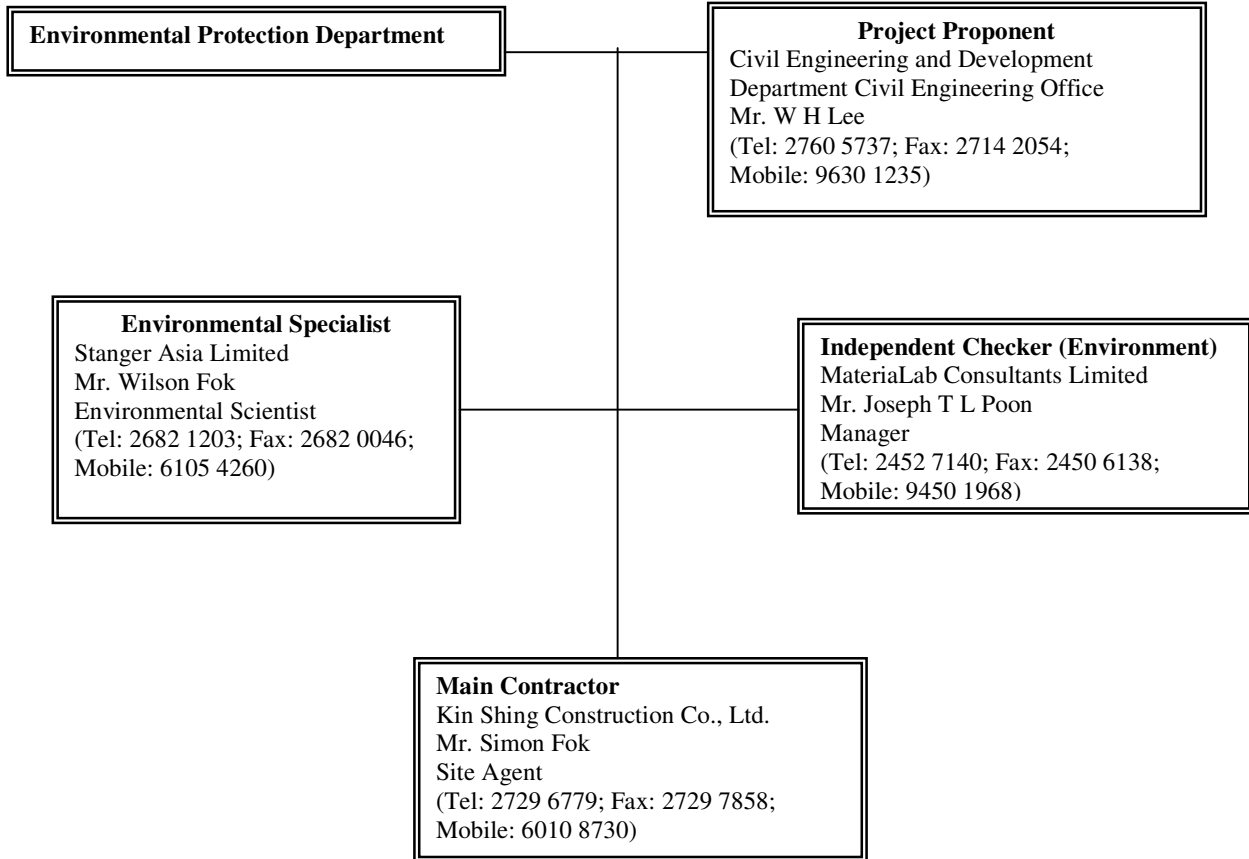

## **Appendix II**

### **Calibration Certificates of the Monitoring Equipment**



**SOMP ENV071: CALIBRATION RECORD OF DISSOLVED OXYGEN,  
SALINITY, CONDUCTIVITY, TEMPERATURE SYSTEM**Equipment No.: EM 6167Model No.: YSI 85Equipment Serial No.: 04L1806Date of Calibration.: 04-04-2005Due Date of Next Calibration.: 04-07-2005Molarity of sodium thiosulphate solution: 0.0250MPotassium Bi-iodate No.: 480Stock Calibration Standard Potassium Chloride No. 625Stock Calibration Check Potassium Chloride No. 648Reference Thermometer No. RF2358***Calibration Check for Dissolved Oxygen***

Standardisation of Sodium Thiosulphate Solution			
Standard Solution	Initial burette reading B, mL	Final burette reading C, mL	Vol. of Na <sub>2</sub> S <sub>2</sub> O <sub>3</sub> used A, mL = (C - B)
Standard 1	0.00	20.10	20.10
Standard 2	0.00	20.00	20.00
Standard 3	0.00	20.00	20.00
Average Value			20.03

Calibration of the Dissolved Oxygen					
Standard Solutions	Initial burette reading B, mL	Final burette reading C, mL	Vol. of Na <sub>2</sub> S <sub>2</sub> O <sub>3</sub> used A, mL = (C - B)	D.O. by titration, mg/L	Meter reading, mg/L
A	0.00	0.00	0.00	0.00	0.00
B	0.00	2.96	2.96	2.96	3.00
C	0.00	5.50	5.50	5.50	5.80
D	0.00	8.98	8.98	9.00	8.90
Allowing deviation : ± 10%					

***Calibration Check for Salinity***

Calibration Check of the Salinity	
Calibration Check Solutions, ppt	Meter reading, ppt
0.0	0.0
10.0	9.9
20.0	19.6
30.0	30.5
40.0	41.1
Allowing deviation : ± 10%	

**Calibration Check for Temperature**

Calibration Check of the Temperature	
Reference Thermometer reading, °C	Meter reading, °C
0.00	0.0
15.10	15.0
25.10	25.0
29.97	30.1
Allowing deviation : $\pm 0.5$ °C	

Tested by :   
Anthony Ma

Checked By :   
Catherine Hung

**SOMP ENV062: CALIBRATION RECORD OF TURBIDIMETER**

Date of Calibration: 29/03/2005

Due Date of Next Calibration: 29/06/2005

Equipment No.: EM 2365

Manufacturer: HACH

Model: 2100 P

Serial No.: 970500014289

Turbidimeter Calibration standard (HACH): No. 1: 20 NTU  
 No. 2: 100 NTU  
 No. 3: 800 NTU

Stock Calibration No.: 896

Three-point calibration accepted: (Y) N

Stock Calibration checking standards No. #895

Turbidity value - Checking standards (NTU)		
Actual value	Measured value	Accepted*: Y/N
0	0	Y
5	5.09	Y
10	10.4	Y
50	51.4	Y
100	99.2	Y
400	389	Y

\*Allowing Deviation: +/- 10%

Tested by:   
 Anthony Ma

Checked by:   
 Catherine Hung

## **Appendix III**

### **Event and Action Plans**

**Event/Action Plan for Water Quality**

EVENT	ACTION			
	ES	IC(E)	ER	CONTRACTOR
Action level				
Action level being exceeded by one sampling day.	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurements to confirm findings;</li> <li>2. Identify source(s) of impacts;</li> <li>3. Inform IC(E) and ER;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IC(E), ER and Contractor;</li> <li>6. Repeat measurements on next day of exceedance.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ES and Contractor on the mitigation measures;</li> <li>2. Review proposals on mitigation measures submitted by Contractor and advise ER accordingly;</li> <li>3. Assess the effectiveness of implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IC(E) on the proposed mitigation measures;</li> <li>2. Make agreement on the mitigation measures to be implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the ER and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with ES and IC(E) and propose mitigation measures to IC(E) and ER;</li> <li>6. Implement the agreed mitigation measures.</li> </ol>
Action level being exceeded by more than one consecutive sampling day.	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurements to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform contractor, IC(E) and ER</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IC(E), ER and Contractor;</li> <li>6. Ensure mitigation measures are implemented;</li> <li>7. Prepare to increase the monitoring frequency to daily;</li> <li>8. Repeat measurements on next day of exceedance.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ES and Contractor on the proposed mitigation measures;</li> <li>2. Review proposals on mitigation measures submitted by Contractor advise ER accordingly;</li> <li>3. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IC(E) on the proposed mitigation measures;</li> <li>2. Make agreement on the mitigation measures to be implemented;</li> <li>3. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Engineer and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with the ES and IC(E) and propose mitigation measures to IC(E) and ER within 3 working days;</li> <li>6. Implement the agreed mitigation measures.</li> </ol>

**Event/Action Plan for Water Quality (Cont'd)**

<b>EVENT</b>	<b>ACTION</b>			
	<b>ES</b>	<b>IC(E)</b>	<b>ER</b>	<b>CONTRACTOR</b>
Limit level				
Limit level being exceeded by one sampling day.	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurements to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform contractor IC(E) and ER;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IC(E), ER and Contractor;</li> <li>6. Ensure mitigation measures are implemented;</li> <li>7. Increase the monitoring frequency to daily until no exceedance of Limit level.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ES and Contractor on the mitigation measures;</li> <li>2. Review proposals on mitigation measures submitted by the Contractor and advise the ER accordingly;</li> <li>3. Assess the effectiveness of implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IC(E), ES and Contractor on the proposed mitigation measures;</li> <li>2. Request Contractor to critically review the working methods;</li> <li>3. Make agreement on the mitigation measures to be implemented;</li> <li>4. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Engineer and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with the ES IC(E) and ER and Propose mitigation measures to IC(E) and ER within 3 working days;</li> <li>6. Implement the agreed mitigation measures.</li> </ol>
Limit level being exceeded by more than one consecutive sampling day.	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurements to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Inform contractor, IC(E) and ER;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Discuss mitigation measures with IC(E), ER and Contractor;</li> <li>6. Ensure mitigation measures are implemented;</li> <li>7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ES and Contractor on the mitigation measures;</li> <li>2. Review proposals on mitigation measures submitted by the Contractor and advise ER accordingly;</li> <li>3. Assess the effectiveness of implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IC(E) ES and Contractor on the proposed mitigation measures;</li> <li>2. Request Contractor to critically review the working methods;</li> <li>3. Make agreement on the mitigation measures to be implemented;</li> <li>4. Assess the effectiveness of the implemented mitigation measures.</li> <li>5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or marine work until no exceedance of Limit level.</li> </ol>	<ol style="list-style-type: none"> <li>1. Inform the Engineer and confirm notification of the non-compliance in writing;</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Discuss with the ES, IC(E) and ER and propose mitigation measures to IC(E) and ER within 3 working days;</li> <li>6. Implement the agreed mitigation measures;</li> <li>7. As directed by the Engineer, slow down or stop all or part of the marine works or construction activities.</li> </ol>

## **Appendix IV**

### **Implementation Status of Mitigation Measures**

## IMPLEMENTATION STATUS OF MITIGATION MEASURES

Area	Mitigation Measures	Implementation Status
Air Quality	Provide a washpit or a wheel washing and/or vehicle cleaning facility at the exits.	Not applicable in this stage
	Provide a hard surfaced road between the wheel washing facilities and any finished road.	Not applicable in this stage
	No burning of construction wastes or vegetation shall be allowed on the Site.	Implemented
	In the process of material handling, any material which has the potential to create dust shall be treated with water or sprayed with wetting agent.	Not applicable in this stage
	Any vehicle with an open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards.	Not applicable in this stage
	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.	Not applicable in this stage
	Stockpiles of sand, aggregate and construction and demolition material greater than 20m <sup>3</sup> shall be enclosed on three sides, with walls extending above the pile and 2 meters beyond the front of the pile.	Not applicable in this stage
	Water sprays shall be provided and used both to dampen stored materials and when receiving raw materials.	Not applicable in this stage
	Clean and water the Site to minimize the fugitive dust emissions.	Implemented
	Furnace, boiler or other plant or equipment or use any fuel that might in any circumstances produce smoke or any other air pollution should not be installed.	Implemented
Noise	All plant and equipment to be used on Site are properly maintained in good operating condition and noisy construction activities shall be effectively sound-reduced by means of silencers, mufflers, acoustic linings or shields, acoustic sheds or screens or other means to avoid disturbance to any nearby noise sensitive receivers.	Implemented
	No excavator mounted breaker shall be used within 125m from any nearby noise sensitive receivers. Use hydraulic concrete crusher whenever applicable.	Implemented
	All construction works should stop on Sundays and General Holidays.	Implemented
Water Quality	Water in wheel washing facilities shall be changed at frequent intervals and sediments shall be removed regularly.	Not applicable in this stage
	The polluted water from the wheel washing facilities would not be discharged into all existing stream courses/drains and nearby waterbodies.	Not applicable in this stage
	All existing stream courses and drains within, and adjacent to the Site should be kept free from any debris and any excavated materials arising from the Works	Implemented
	Chemicals and concrete agitator washings should not be deposited in watercourses.	Implemented
	The effluent shall comply with the standards stated in the "Technical Memorandum on Standards and Effluent discharges into Drainage and Sewerage Systems, Inland and Coastal Waters" for the appropriate Water Control Zone.	Implemented
	No spoil or debris of any kind is allowed to be pushed, washed down, fall or be deposited on land or on the seabed adjacent to the Site.	Implemented



## IMPLEMENTATION STATUS OF MITIGATION MEASURES

Area	Mitigation Measures	Implementation Status
	Maintain any existing site drainage system at all times including removal of solids in sand traps, manholes and stream beds.	Implemented
	Material from any earthworks should not be washed into the drainage system.	Implemented
	Silt curtain shall be provided during all demolition works and piling works with the Site.	Not applicable in this stage
	Silt curtain shall be formed from tough, abrasion-resistant permeable membranes suitable for the purpose, supported on floating booms in such a way as to ensure that the passage of turbid water to the surrounding water shall be restricted.	Not applicable in this stage
	No dredging and spoil dumping shall be conducted.	Not applicable in this stage
Ecology	Marker buoys shall be set up to indicate the location of the "Coral Exclusion Zone". All working vessels shall be restricted to encroach the "Coral Exclusion Zone"	Implemented
	No overloading of the working barges during operation and no movement of the working barges, particularly close to the pier and shallow areas, during low tide should be allowed.	Not applicable in this stage
	No coral shall be enclosed by the silt curtain.	Not applicable in this stage
Waste	All excavated materials should be sorted to recover the inert portions for reuse on site or disposal to designated outlets.	Not applicable in this stage
	All metals should be recovered on site for collection by recycling contractors.	Not applicable in this stage
	All cardboard and paper packaging should be recovered on site, properly stockpiled in dry condition and covered to prevent cross contamination by other C&D materials.	Not applicable in this stage
	All demolition debris from demolition works should be sorted to recover on site broken concrete, reinforcement bars, mechanical and electrical fittings as well as other building services fittings/materials that have established recycling outlets.	Not applicable in this stage

**Appendix V**

**Water Quality Monitoring Data**

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 04/04/2005

Weather Condition: Cloudy

Ambient Temperature, °C: 21

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks	
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average		Depth Average		
MW1 S	14:00	Stable	7	1	18.6	18.6	7.51	7.50	7.46	99.4	98.5	97.1	32.8	32.8	0.81	0.77	0.75	7	6	6.1	
MW1 M				3.5	17.7	17.7	7.40	7.41	7.46	95.3	95.1	95.8	32.8	32.8	0.70	0.64		5	6		
MW1 B				6	17.7	17.7	7.47	7.45	7.46	95.8	95.7	95.8	32.8	32.8	0.77	0.82		7	6		
MW2 S	14:30	Stable	11	1	18.3	18.3	7.66	7.76	7.73	98.7	99.0	99.3	32.7	32.7	0.96	0.91	0.64	6	5	6.5	
MW2 M				5.5	17.8	17.8	7.74	7.75	7.73	99.8	99.5	94.8	32.6	32.7	0.94	0.89		6	6		
MW2 B				10	17.9	17.9	7.40	7.45	7.43	94.8	94.7	94.8	32.8	32.8	0.70	0.64		7	8		
CW1 S	14:45	Stable	5	1	18.7	18.7	7.54	7.53	7.54	98.8	99.2	99.0	32.8	32.8	0.84	0.80	0.71	6	5	7.2	
CW1 M																					
CW1 B				4	18.5	18.5	7.32	7.31	7.32	97.4	96.7	97.1	32.7	32.7	0.62	0.58		10	8		
CW2 S	14:35	Stable	11	1	18.4	18.4	7.86	7.91	7.74	100.7	100.8	100.5	32.8	32.8	0.96	0.91	0.82	9	12	8.0	
CW2 M				5.5	17.7	17.7	7.62	7.58	7.74	100.4	99.9	92.5	32.7	32.7	0.92	0.97		6	6		
CW2 B				10	17.5	17.5	7.12	7.11	7.12	92.9	92.1	92.5	32.8	32.8	0.52	0.63		7	8		

Equipment used: Dissolved Oxygen Meter: EM 6167

Turbidity Meter: EM 2305

Salinity Meter: EM 6167

Thermometer: EM 6167

EM 6167

EM 2305

EM 6167

EM 6167

Calibration Check: 0mg/L OK 100%: OK

Calibration Check: 5.39 46.1 497 NTU

Calibration Check: 58.7 mS

Sampled By: Anthony Ma

Checked By: AM

Date: 6/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers Client: Kin Shing Construction Co., Ltd. Job No. 1518.3

Date of Sampling: 04/04/2005 Weather Condition: Sunny Ambient Temperature, °C: 20 Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks	
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average	Depth Average		
MW1 S		Stable	6	1	18.4	18.4	7.40	7.46	7.39	94.2	94.5	94.3	32.6	32.6	0.70	0.76	0.69	6	5	5.4	
MW1 M	09:25			3	18.4	18.4	7.33	7.35		94.1	94.2		32.6	32.6	0.63	0.65		6	5		
MW1 B				5	17.9	17.9	7.38	7.38	7.38	95.7	95.5	95.6	32.6	32.6	0.68	0.72		5	6		
MW2 S		Stable	10	1	18.5	18.5	7.30	7.31	7.26	95.2	95.3	95.9	32.4	32.4	0.60	0.66	0.53	6	7	5.6	
MW2 M	09:15			5	17.8	17.8	7.19	7.22		92.8	92.4		32.5	32.5	0.49	0.52		4	6		
MW2 B				9	17.7	17.7	7.13	7.12	7.13	91.6	91.4	91.5	32.7	32.7	0.43	0.46		6	6		
CW1 S		Stable	4	1	18.5	18.5	7.15	7.15	7.15	92.6	92.7	92.7	32.6	32.6	0.45	0.50	0.55	6	8	5.6	
CW1 M	09:30																				
CW1 B				3	18.4	18.4	7.22	7.21	7.22	95.5	94.8	95.2	32.6	32.6	0.52	0.64		5	5		
CW2 S		Stable	10	1	18.5	18.5	7.47	7.45	7.52	97.8	98.8	98.1	32.7	32.7	0.77	0.81	0.89	8	8	8.2	
CW2 M	09:20			5	18.3	18.3	7.57	7.58		99.1	98.5		32.6	32.6	0.87	0.94		11	10		
CW2 B				9	17.7	17.7	7.73	7.67	7.70	100.5	99.8	100.2	32.6	32.6	0.93	0.99		8	7		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2355 Calibration Check: 5.39, 48.1, 497 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma  
 Checked By: [Signature]  
 Date: 6/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 06/04/2005 Weather Condition: Sunny Ambient Temperature, °C: 24 Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Depth Average	Remarks	
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average			
MW1 S		Small wave	7	1	19.3	19.3	7.53	7.51	7.50	100.0	100.4	100.4	32.9	32.9	0.54	0.67	0.89	5	6	6.1	
MW1 M	16:30			3.5	18.0	18.0	7.56	7.78		101.0	100.1		32.9	32.8	0.70	0.62		6	5		
MW1 B				6	17.8	17.8	7.63	7.54	7.59	101.3	99.7	100.5	33.0	33.0	0.74	0.84		7	8		
MW2 S		Small wave	9	1	19.5	19.5	7.46	7.60	7.54	99.9	99.0	99.2	32.9	32.9	0.86	0.92	0.90	5	5	6.2	
MW2 M	16:00			4.5	18.0	18.0	7.30	7.81		99.1	98.6		32.9	32.9	1.09	0.97		8	8		
MW2 B				8	17.7	17.7	7.32	7.29	7.31	97.6	95.8	96.7	33.0	33.0	0.83	0.75		6	5		
CW1 S		Small wave	4	1	19.3	19.3	7.56	7.56	7.56	96.6	97.7	97.3	33.0	33.0	0.68	0.76	0.77	6	7	6.3	
CW1 M	16:45																				
CW1 B				3	18.7	18.6	7.86	8.03	7.95	103.8	105.2	104.5	33.0	33.0	0.79	0.83		6	7		
CW2 S		Small wave	10	1	19.3	19.3	7.81	7.87	8.07	101.9	102.4	102.2	32.9	32.9	0.76	0.58	0.79	7	8	7.0	
CW2 M	16:15			5	18.2	18.2	8.23	8.36		102.6	101.6		32.9	32.9	0.88	0.73		8	5		
CW2 B				9	17.7	17.7	7.78	7.89	7.84	102.3	101.0	101.7	33.0	33.0	0.88	0.93		6	9		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L, OK 100%, OK  
 Turbidity Meter: EM 2366 Calibration Check: 5.21, 50.8, 501 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.1 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 8/4/05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 06/04/2005 Weather Condition: Sunny Ambient Temperature, °C: 23 Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average	Depth Average	
MW1 S	12:30	Stable	6	1	20.2	20.2	8.00	8.02	7.75	100.4	100.6	100.7	32.8	32.8	0.71	0.53	0.62	4	5	6.8
MW1 M				3	18.1	18.2	7.56	7.41	100.3	101.3	32.9	32.8	0.59	0.66	8	9				
MW1 B				5	18.0	18.0	7.52	7.48	7.50	96.0	96.0	96.0	32.8	32.8	0.65	0.60		7	9	
MW2 S	12:10	Stable	8	1	19.1	19.1	7.52	7.43	7.50	100.6	99.4	98.6	32.9	32.9	0.67	0.65	0.67	4	4	6.7
MW2 M				4	18.8	18.8	7.54	7.50	97.0	96.1	33.1	33.1	0.57	0.70	9	8				
MW2 B				7	18.3	18.3	7.55	7.54	7.55	97.5	96.8	97.2	32.9	32.9	0.73	0.72		8	8	
CW1 S	12:20	Stable	4	1	19.6	19.6	7.69	7.85	7.77	99.6	99.6	99.6	32.8	32.8	0.69	0.61	0.70	8	7	7.2
CW1 M				3	18.2	18.2	7.71	7.72	7.72	95.8	98.9	97.4	32.9	32.9	0.77	0.72		8	6	
CW1 B																				
CW2 S	12:45	Stable	9	1	19.3	19.1	7.35	7.36	7.27	95.7	96.1	96.0	32.9	32.9	0.55	0.59	0.59	5	8	7.3
CW2 M				4.5	18.1	18.1	7.27	7.10	94.8	97.3	32.9	32.9	0.52	0.52	8	9				
CW2 B				8	17.9	17.8	6.97	7.03	7.00	92.9	91.7	92.3	32.8	32.8	0.66	0.59		9	6	

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L OK 100% OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.21, 50.8 501 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 8/4/05

### Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 06/04/2005

Weather Condition: Cloudy

Ambient Temperature: °C 21

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C			Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/l		Remarks
					a	b	Average	a	b	Average	a	b	Average	a	b	Average	Depth	Average			
MK1 S		stable	7	1	18.1	18.5	7.61	7.58	7.50	98.5	98.6	94.9	32.8	32.8	0.85	0.79	0.72	<3	<3	<3	
MK1 M	15:10			3.5	17.8	17.8	7.40	7.41	96.3	86.1	32.8	32.8	0.76	0.68	<3	3					
MK1 B				6	17.5	17.5	6.86	6.84	6.85	89.7	87.8	88.8	32.9	32.9	0.65	0.57		<3	<3		
MK2 S		stable	16	1	18.0	18.0	7.64	7.65	7.37	96.9	96.7	94.3	32.8	32.8	0.74	0.69	0.84	<3	<3	<3	
MK2 M	15:20			8	17.5	17.5	7.10	7.09	91.8	91.7	32.8	32.8	0.91	0.84	3	3					
MK2 B				15	17.3	17.3	6.85	6.87	6.86	84.9	94.6	89.8	33.0	33.0	0.96	0.91		<3	4		
MK3 S		stable	8	1	18.1	18.1	7.86	7.88	7.80	99.0	99.7	100.0	32.8	32.8	0.71	0.68	0.82	<3	<3	<3	
MK3 M	14:50			4	17.8	17.8	7.65	7.64	100.8	100.3	32.8	32.8	0.82	0.86	3	<3					
MK3 B				7	17.5	17.5	6.96	6.92	6.94	91.0	90.3	90.7	32.8	32.9	0.99	0.85		<3	<3		
MK4 S		stable	12	1	17.9	17.9	7.60	7.57	7.37	100.4	99.6	96.6	32.8	32.8	0.65	0.60	0.74	<3	<3	<3	
MK4 M	15:00			6	17.5	17.5	7.17	7.14	93.6	92.9	32.8	32.8	0.88	0.82	3	3					
MK4 B				11	17.3	17.3	6.85	6.83	6.84	86.9	86.4	86.7	32.9	32.9	0.71	0.75		<3	<3		
CK1 S		stable	18	1	18.2	18.2	8.13	8.10	8.02	103.5	104.0	102.2	32.8	32.8	0.81	0.87	0.84	<3	3	3.0	
CK1 M	15:30			9	18.1	18.1	7.86	7.92	100.8	100.6	32.8	32.8	0.92	0.95	<3	3					
CK1 B				17	17.4	17.4	6.81	6.80	6.81	87.4	86.9	87.2	33.0	33.0	0.73	0.77		3	3		
CK2 S		stable	20	1	18.1	18.1	7.97	7.98	7.58	102.6	102.8	99.1	32.8	32.8	0.66	0.69	0.77	3	<3	<3	
CK2 M	15:40			10	17.7	17.7	7.40	7.38	96.0	94.9	32.8	32.8	0.75	0.79	<3	<3					
CK2 B				19	17.3	17.3	6.78	6.79	6.79	86.7	86.6	86.7	33.0	33.0	0.88	0.84		<3	<3		

Equipment used: Dissolved Oxygen Meter: EM 6167

Turbidity Meter: EM 2365

Salinity Meter: EM 6167

Thermometer: EM 6167

Calibration Check: 0mg/L: OK 100%: OK

Calibration Check: 5.21, 50.8, 501 NTU

Calibration Check: 58.7 mS

Sampled By: Anthony Ma

Checked By: [Signature]

Date: 8/4/05

## Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Kc Lau Wan Public Piers

Client: Kin Shing Construction Co. Ltd. Job No.: 1618.3

Date of Sampling: 06/04/2005

Weather Condition: Sunny

Ambient Temperature, °C: 21

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L		Average	Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Depth Average	Remarks	
					a	b	a	b		a	b	Average	a	b	a	b	Average				
MK1 S	11:05	stable	6	1	18.5	18.5	7.27	7.34	7.39	94.6	94.6	94.9	32.9	32.9	0.55	0.63	0.67	3.0	3.3	<3	
MK1 M				3	18.3	18.3	7.57	7.36	7.36	95.0	95.5	94.9	32.9	32.9	0.84	0.68		<3	<3		
MK1 B				5	18.1	18.1	7.43	7.57	7.50	94.4	99.5	97.0	32.9	32.9	0.57	0.72		<3	<3		
MK2 S	11:15	stable	15	1	18.5	18.5	7.49	7.49	7.70	96.7	96.4	93.3	32.9	32.9	0.62	0.74	0.67	<3	3.0	<3	
MK2 M				7.5	17.8	17.8	7.93	7.88	7.88	90.7	91.2	93.3	32.9	32.9	0.75	0.67		<3	<3		
MK2 B				14	17.5	17.5	6.90	6.67	6.79	90.0	89.3	89.7	33.0	33.0	0.59	0.66		3.0	<3		
MK3 S	10:45	stable	6	1	18.8	18.6	7.45	7.53	7.62	96.3	96.8	98.4	32.8	32.8	0.52	0.54	0.62	<3	3.5	<3	
MK3 M				3	18.4	18.4	7.58	7.90	7.90	99.7	100.7	98.4	32.8	32.8	0.67	0.63		<3	<3		
MK3 B				5	17.9	17.9	7.55	7.50	7.53	101.1	102.2	101.7	32.8	32.8	0.67	0.70		3.5	<3		
MK4 S	10:55	stable	12	1	18.6	18.6	7.16	7.12	7.36	92.2	92.5	96.1	32.9	32.8	0.56	0.70	0.64	<3	<3	<3	
MK4 M				6	17.7	17.7	7.60	7.57	7.57	98.7	100.9	96.1	32.9	32.9	0.48	0.65		<3	<3		
MK4 B				11	17.6	17.6	6.89	6.67	6.78	84.9	85.5	85.2	33.0	33.0	0.73	0.73		<3	<3		
CK1 S	11:30	stable	19	1	18.6	18.6	7.74	7.72	7.81	101.1	101.5	99.2	32.9	32.9	0.59	0.66	0.66	<3	<3	<3	
CK1 M				9.5	17.8	17.8	7.83	7.96	7.96	97.2	96.9	99.2	32.9	32.9	0.56	0.73		<3	<3		
CK1 B				18	17.6	17.6	7.35	7.26	7.31	98.5	98.0	98.3	33.1	33.1	0.76	0.68		<3	<3		
CK2 S	11:40	stable	19	1	18.7	18.7	8.02	8.02	7.91	102.4	103.8	101.3	32.9	32.9	0.68	0.63	0.74	<3	<3	<3	
CK2 M				9.5	18.2	18.0	7.85	7.76	7.76	99.3	99.7	101.3	32.9	32.9	0.63	0.79		3.0	<3		
CK2 B				18	17.6	17.6	6.87	6.89	6.88	99.4	98.0	98.7	33.0	33.0	0.77	0.74		3.2	3.0		

Equipment used: Dissolved Oxygen Meter: EM 6167  
 Turbidity Meter: EM 2365  
 Salinity Meter: EM 6167  
 Thermometer: EM 6167

Calibration Check: 0mg/L: OK 100% OK  
 Calibration Check: 5.21, 50.8, 501 NTU  
 Calibration Check: 58.7 mS

Sampled By: Anthony Ma  
 Checked By: *[Signature]*  
 Date: 8/4/05



### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 08/04/2005

Weather Condition: Cloudy

Ambient Temperature: °C: 22

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks		
					a	b	a	b	Average	a	b	Average	a	b	Average	Depth	Average				
MW1 S		Stable	7	1	21.3	21.3	7.31	7.15	7.49	97.9	99.2	100.2	32.9	32.9	0.56	0.60	0.74	4	5	5.6	
MW1 M	17:20			3.5	18.7	18.7	7.73	7.78		101.8	101.7		32.8	32.9	0.79	0.84		8	7		
MW1 B				6	18.3	18.3	7.62	7.60	7.61	102.3	100.5	101.4	32.9	32.9	0.84	0.78		5	5		
MW2 S		Stable	7	1	20.0	20.0	7.65	7.67	7.66	100.5	101.3	103.7	33.0	33.0	0.49	0.47	0.68	4	4	5.1	
MW2 M	17:00			3.5	18.2	18.2	8.27	8.26		105.3	105.6		32.9	32.9	0.68	0.71		7	6		
MW2 B				6	18.0	18.0	7.86	7.84	7.85	104.8	103.1	104.0	32.9	32.9	0.84	0.89		5	5		
CW1 S		Stable	4	1	21.3	21.3	7.26	7.25	7.26	99.0	99.1	99.1	32.8	32.8	0.59	0.62	0.66	7	8	6.7	
CW1 M	17:30																				
CW1 B				3	18.6	18.8	7.47	7.44	7.46	99.8	98.6	99.2	32.9	32.9	0.71	0.78		6	5		
CW2 S		Stable	9	1	19.2	19.2	8.13	8.14	8.04	107.4	107.3	109.0	33.0	33.0	0.66	0.70	0.77	5	6	5.2	
CW2 M	17:10			4.5	18.4	18.4	7.47	8.42		110.5	110.8		32.9	32.9	0.74	0.78		6	5		
CW2 B				8	18.0	18.0	7.61	6.67	7.14	95.0	85.8	80.4	33.0	33.0	0.86	0.90		5	5		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L, OK 100%, OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.31, 51.8, 510 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma  
 Checked By: [Signature]  
 Date: 10/4/05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No: 1618.3

Date of Sampling: 08/04/2005

Weather Condition: Cloudy

Ambient Temperature, °C: 23

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Depth Average	Remarks		
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	4			5	
MW1 S	11:50	Stable	7	1	19.4	19.4	7.78	7.79	8.00	101.3	101.5	103.9	33.0	33.0	0.47	0.52	0.60	4	5	6.0		
MW1 M				3.5	19.0	19.0	8.21	8.20		106.1	106.6		32.9	33.0	0.58	0.61		6	5			
MW1 B				6	18.4	18.4	8.26	8.22		8.24	107.4		107.8	107.6	32.9	32.9		0.69	0.74			8
MW2 S	11:30	Stable	9	1	20.2	20.2	7.37	7.44	7.81	99.5	99.8	102.9	32.6	32.6	0.57	0.54	0.67	5	6	6.4		
MW2 M				4.5	18.4	18.4	8.21	8.20		105.8	106.4		32.7	32.7	0.64	0.60		6	6			
MW2 B				8	18.2	18.2	8.04	8.03		8.04	104.0		103.9	104.0	32.8	32.9		0.77	0.76			8
CW1 S	12:00	Stable	4	1	19.9	19.9	7.43	7.44	7.44	99.7	99.3	99.5	32.9	32.9	0.76	0.64	0.96	8	7	6.8		
CW1 M																			6			6
CW1 B				3	18.0	18.7	7.67	7.61		7.64	102.0		102.1	102.1	32.9	32.9		0.91	0.92			
CW2 S	11:40	Stable	10	1	19.8	19.8	7.93	7.93	8.23	105.3	105.5	106.5	32.9	32.9	0.82	0.77	0.74	4	4	5.0		
CW2 M				5	18.4	18.4	8.56	8.49		111.4	111.7		32.9	32.9	0.74	0.78		4	5			
CW2 B				9	18.0	18.0	7.89	7.88		7.89	102.5		102.2	102.4	33.0	33.0		0.65	0.70			7

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: Dmg/L: OK 100% OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.31, 51.8, 510 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma  
 Checked By: [Signature]  
 Date: 10/4/05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 11/04/2005 Weather Condition: Cloudy Ambient Temperature, °C: 25 Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L		Average	Dissolved Oxygen, %		Salinity, ppt		Turbidity, NTU		Average	Suspended Solids, mg/L		Depth Average	Remarks		
					a	b	a	b		a	b	a	b	a	b		a	b				
MW1 S		Stable	7	1	20.1	20.1	7.59	7.60	7.69	102.0	101.2	102.8	33.1	33.1	0.59	0.53	0.73	3	4	4.3		
MW1 M	08:20			3.5	19.8	19.8	7.78	7.77		104.1	103.8		33.1	33.1	0.78	0.71		4	5			
MW1 B				6	19.2	19.2	7.12	7.09	7.11	94.4	94.5	94.5	33.1	33.1	0.92	0.86		4	5			
MW2 S		Stable	10	1	19.9	19.9	7.57	7.50	7.64	103.5	103.1	103.9	33.0	33.0	0.57	0.51	0.67	4	5	3.9		
MW2 M	08:00			5	19.6	19.6	7.74	7.75		105.0	103.9		33.1	33.1	0.74	0.69		5	4			
MW2 B				9	19.2	19.2	7.79	7.79	7.79	102.8	102.9	102.9	33.1	33.1	0.79	0.71		3	3			
CW1 S		Stable	4	1	20.2	20.2	7.73	7.72	7.73	101.6	102.8	102.2	33.1	33.1	0.73	0.78	0.83	4	4	4.0		
CW1 M	08:25																					
CW1 B				3	20.1	20.1	7.28	7.21	7.25	98.8	98.7	98.8	33.1	33.1	0.88	0.94		4	5			
CW2 S		Stable	10	1	20.0	20.0	7.50	7.45	7.58	102.0	102.1	102.0	33.1	33.1	0.50	0.57	0.59	4	3	4.0		
CW2 M	08:10			5	19.3	19.3	7.65	7.70		102.3	101.7		33.1	33.1	0.65	0.69		4	4			
CW2 B				9	19.1	19.1	7.54	7.51	7.53	101.5	100.3	100.9	33.1	33.1	0.54	0.58		5	4			

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.11, 49.3, 498 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma  
 Checked By: [Signature]  
 Date: 10/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 11/04/2005 Weather Condition: Cloudy Ambient Temperature °C: 26 Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/l		Remarks		
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	6		7	Depth Average
MW1 S	14:15	Stable	7	1	20.5	20.5	7.27	7.28	7.46	98.8	96.3	99.6	33.1	33.1	0.78	0.72	0.82	6	7	6.4	
MW1 M				3.5	19.9	19.9	7.59	7.71	7.46	100.9	100.5	99.6	33.1	33.1	0.82	0.76		6	5		
MW1 B				6	19.7	19.7	7.63	7.68	7.66	99.5	100.1	99.8	33.2	33.2	0.94	0.88		8	8		
MW2 S	14:00	Stable	9	1	20.1	20.1	7.63	7.53	7.38	100.1	101.5	100.3	33.2	33.1	0.68	0.61	0.75	6	5	6.0	
MW2 M				4.5	19.7	19.7	7.20	7.16	7.38	100.0	99.4	100.3	33.1	33.1	0.79	0.73		6	5		
MW2 B				8	19.1	19.1	7.46	7.48	7.48	97.2	97.6	97.4	33.1	33.2	0.86	0.80		7	8		
CW1 S	14:25	Stable	4	1	21.5	21.5	7.21	7.16	7.19	99.6	99.1	99.4	33.0	33.0	0.77	0.76	0.83	6	5	5.9	
CW1 M																					
CW1 B				3	19.9	19.8	7.43	7.31	7.37	101.8	102.4	102.1	32.9	33.0	0.86	0.93		7	6		
CW2 S	14:05	Stable	9	1	19.6	19.6	7.82	7.82	7.93	104.4	104.2	105.5	33.2	33.2	0.67	0.60	0.77	4	5	4.4	
CW2 M				4.5	19.3	19.3	8.04	8.05	7.93	106.5	106.7	105.5	33.2	33.2	0.81	0.74		4	3		
CW2 B				8	19.1	19.1	7.62	7.60	7.61	99.5	99.3	99.4	33.2	33.2	0.92	0.88		5	6		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.11, 49.3, 498 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma  
 Checked By: [Signature]  
 Date: 10/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 19/04/2005

Weather Condition: Sunny

Ambient Temperature °C: 28

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Depth Average	Remarks			
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average						
MW1 S		Samll Wave	7	1	22.1	22.1	7.14	7.16	7.01	96.5	96.9	95.7	33.3	33.3	1.06	0.99	0.67	5	5	6.2				
MW1 M	14:00			3.5	20.3	20.3	6.87	6.86		94.6	94.7		33.3	33.3	0.77	0.84		6	6					
MW1 B				6	20.1	20.1	7.07	7.03		7.05	94.7		94.8	94.8	33.3	33.4		0.75	0.80		6	8		
MW2 S		Samll Wave	10	1	21.4	21.4	6.89	6.90	7.05	94.8	95.0	95.1	33.2	33.2	1.09	1.05	1.10	5	6	6.1				
MW2 M	13:30			5	21.1	21.0	7.20	7.21		95.4	95.3		33.2	33.3	0.85	0.79		6	6					
MW2 B				9	20.0	20.0	7.14	7.15		7.15	95.4		95.3	95.4	33.3	33.4		1.40	1.42		7	7		
CW1 S		Samll Wave	5	1	22.0	22.0	7.36	7.28	7.32	101.3	101.6	101.5	33.3	33.2	0.86	0.94	0.93	6	6	6.2				
CW1 M	14:15																							
CW1 B				4	21.7	21.6	7.17	7.19		7.18	97.2		97.4	97.3	33.2	33.2		0.92	0.98		6	7		
CW2 S		Samll Wave	12	1	21.4	21.4	6.66	6.68	6.83	93.3	93.2	94.2	33.2	33.2	0.86	0.95	1.32	7	6	7.0				
CW2 M	13:45			6	20.7	20.7	7.00	6.99		95.1	95.0		33.2	33.2	1.32	1.40		7	5					
CW2 B				11	20.1	20.1	7.24	7.24		7.24	95.9		95.0	96.0	33.3	33.3		1.74	1.64		9	9		

Equipment used:

Dissolved Oxygen Meter:	EM	6167	Calibration Check:	0mg/L: OK	100%: OK
Turbidity Meter:	EM	2365	Calibration Check:	5, 10, 49.4	498 NTU
Salinity Meter:	EM	6167	Calibration Check:	58.7	mS
Thermometer:	EM	6167			

Sampled By: Y.C. Cheng

Checked By: *[Signature]*

Date: 20/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 19/04/2005

Weather Condition: Sunny

Ambient Temperature, °C: 24

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C			Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks
					a	b	Average	a	b	Average	a	b	Average	a	b	Average	Depth	Average			
MW1 S	09:50	Small Wave	6	1	20.6	20.6	6.93	6.94	6.96	96.0	96.2	95.4	33.2	33.2	0.84	0.88	0.98	6	5	6.3	
MW1 M				3	20.4	20.4	6.97	6.99	94.6	94.8	33.2	33.2	0.77	0.74	6	6					
MW1 B				5	20.4	20.4	6.92	6.94	6.93	94.8	95.0	94.9	33.2	33.4	1.35	1.31		7	8		
MW2 S	09:30	Small Wave	9	1	21.1	21.1	6.79	6.80	6.99	95.9	96.0	95.8	33.1	33.1	0.98	1.06	0.96	5	5	6.2	
MW2 M				4.5	19.8	19.9	7.18	7.20	95.7	95.7	33.2	33.4	1.03	1.10	6	6					
MW2 B				8	19.7	19.7	7.14	7.14	7.14	88.0	89.1	89.0	33.3	33.4	0.73	0.85		9	7		
CW1 S	10:00	Small Wave	4	1	21.0	21.0	6.91	6.93	6.92	96.5	96.7	96.6	33.1	33.1	0.81	0.76	0.98	6	5	6.2	
CW1 M																					
CW1 B				3	20.9	20.9	6.94	6.96	6.95	95.9	96.4	96.2	33.2	33.1	1.12	1.24		7	7		
CW2 S	09:40	Small Wave	10	1	20.7	20.7	6.99	6.95	7.14	95.7	95.8	93.2	33.1	33.1	1.07	1.01	0.93	5	7	5.1	
CW2 M				5	19.7	19.7	7.29	7.31	90.4	90.7	33.2	33.2	0.98	0.91	5	6					
CW2 B				9	19.5	19.5	6.92	6.94	6.93	92.4	92.2	92.3	33.3	33.3	0.82	0.78		4	5		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.10, 49.4, 498 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: *[Signature]*  
 Date: 20/4/05

Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 19/04/2005

Weather Condition: Sunny

Ambient Temperature, °C: 28

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C			Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Depth Average	Remarks
					a	b	Average	a	b	Average	a	b	Average	a	b	Average					
MK1 S	15:30	stable	7	1	20.4	20.4	6.95	6.98	6.96	91.0	92.5	92.0	33.3	33.3	0.62	0.57	0.81	5	5	4.9	
MK1 M				3.5	20.2	20.2	6.90	6.99	6.94	91.5	91.2	91.4	33.4	33.4	0.70	0.77	0.81	4	4		
MK1 B				6	19.9	19.9	6.95	6.92	6.94	91.5	91.2	91.4	33.4	33.4	0.70	0.77	0.81	6	6		
MK2 S	15:41	stable	15	1	20.3	20.3	7.10	7.05	6.97	95.8	96.0	96.0	33.2	33.2	0.56	0.63	0.62	5	6	5.7	
MK2 M				7.5	20.0	19.9	6.89	6.85	6.93	94.2	93.8	94.0	33.3	33.3	0.68	0.71	0.62	6	7		
MK2 B				14	19.5	19.6	7.02	7.04	7.03	91.5	91.8	91.7	33.3	33.3	0.54	0.58	0.62	5	6		
MK3 S	15:00	stable	7	1	20.6	20.6	7.16	7.18	7.04	95.4	95.1	93.1	33.3	33.3	0.56	0.59	0.69	6	6	6.2	
MK3 M				3.5	20.3	20.3	6.92	6.91	6.91	91.1	90.8	91.0	33.2	33.2	0.56	0.53	0.69	6	6		
MK3 B				6	20.2	20.2	6.95	6.93	6.94	93.3	93.5	93.4	33.3	33.4	0.90	0.98	0.69	8	6		
MK4 S	15:15	stable	14	1	20.5	20.5	6.78	7.02	7.08	96.0	96.6	95.8	33.2	33.2	0.66	0.59	0.58	7	8	5.9	
MK4 M				7	20.0	20.0	7.25	7.26	7.26	96.0	95.7	95.8	33.3	33.3	0.56	0.64	0.58	6	5		
MK4 B				13	19.6	19.6	7.20	7.16	7.18	97.6	97.7	97.7	33.3	33.3	0.54	0.49	0.58	6	7		
CK1 S	15:00	stable	21	1	20.9	20.9	7.21	7.20	7.13	101.5	101.7	97.8	33.2	33.2	0.64	0.64	0.60	6	6	8.1	
CK1 M				10.5	20.5	20.5	7.04	7.05	7.05	93.7	94.1	93.9	33.5	33.4	0.57	0.61	0.60	5	7		
CK1 B				20	20.2	20.2	7.00	7.01	7.01	95.2	95.3	95.3	33.5	33.5	0.77	0.74	0.60	7	7		
CK2 S	15:45	stable	21	1	21.1	21.1	7.16	7.13	7.13	98.6	98.9	96.4	33.3	33.3	0.55	0.57	0.74	6	5	6.5	
CK2 M				10.5	20.9	20.9	7.11	7.13	7.12	97.8	98.1	97.9	33.4	33.4	0.77	0.83	0.74	6	7		
CK2 B				20	20.7	20.6	7.08	7.11	7.10	98.3	98.7	98.5	33.3	33.3	0.67	0.64	0.74	8	8		

Equipment used: Dissolved Oxygen Meter: EM 6167  
 Turbidity Meter: EM 2365  
 Salinity Meter: EM 6167  
 Thermometer: EM 6167

Calibration Check: 0mg/L: OK 100%: OK  
 Calibration Check: 5.15, 50.9, 500 NTU  
 Calibration Check: 58.6 mS

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 21/4/05

### Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers      Client: Kin Shing Construction Co., Ltd.      Job No.: 1618.3  
 Date of Sampling: 19/04/2005      Weather Condition: Sunny      Ambient Temperature, °C: 24      Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks	
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	a		b
MK1 S	11:15	Small wave	6	1	20.8	20.8	6.94	6.95	6.96	92.3	92.4	92.3	33.3	33.4	0.60	0.56	0.79	4	5	5.1
MK1 M				3	20.4	20.4	6.95	6.98		92.4	92.1		33.3	33.4	1.01	1.10		5	6	
MK1 B				5	20.1	20.1	6.77	6.86		6.82	90.0		91.6	90.6	33.2	33.2		0.71	0.78	
MK2 S	11:30	Small wave	14	1	20.4	20.4	6.99	6.99	6.92	93.0	93.0	92.0	33.2	33.2	0.71	0.68	0.86	5	5	5.6
MK2 M				7	20.1	20.1	6.83	6.85		90.8	91.1		33.3	33.4	0.76	0.82		7	7	
MK2 B				13	20.0	20.0	6.90	6.91		6.91	91.8		91.9	91.8	33.2	33.1		1.14	1.06	
MK3 S	10:45	Small wave	6	1	20.6	20.6	7.02	7.05	6.93	93.4	93.8	92.7	33.1	33.1	0.42	0.47	0.79	5	6	5.9
MK3 M				3	20.1	20.1	6.80	6.85		91.8	92.0		33.2	33.3	0.68	0.74		6	6	
MK3 B				5	20.0	20.0	6.79	6.72		6.76	91.5		91.4	91.5	33.3	33.4		1.16	1.27	
MK4 S	11:00	Small wave	13	1	20.6	20.6	6.93	6.95	6.91	92.2	92.4	91.9	33.2	33.1	0.65	0.72	0.75	6	7	6.1
MK4 M				6.5	20.1	20.1	6.88	6.89		91.5	91.6		33.3	33.4	0.70	0.73		6	5	
MK4 B				12	19.8	19.8	6.80	6.86		6.83	91.8		91.2	91.5	33.4	33.4		0.82	0.88	
CK1 S	12:00	Small wave	20	1	20.7	20.7	7.10	7.09	7.12	93.6	93.7	93.4	33.2	33.2	0.61	0.65	0.73	5	5	6.2
CK1 M				10	20.3	20.2	7.14	7.16		93.1	93.0		33.2	33.1	0.68	0.71		6	8	
CK1 B				19	19.7	19.6	7.06	7.04		7.05	92.7		92.8	92.8	33.0	33.1		0.83	0.87	
CK2 S	11:49	Small wave	20	1	20.7	20.7	7.12	7.14	7.17	94.9	85.0	89.8	33.2	33.3	0.55	0.61	0.85	6	5	5.8
CK2 M				10	20.3	20.3	7.21	7.21		94.5	84.6		33.2	33.2	0.89	0.91		5	7	
CK2 B				19	19.6	19.6	7.02	7.04		7.03	93.4		93.5	93.5	33.1	33.1		1.03	1.08	

Equipment used: Dissolved Oxygen Meter: EM 6167      Calibration Check: Dmg/L OK      100%: OK  
 Turbidity Meter: EM 2365      Calibration Check: 5.15, 50.9, 500      NTU  
 Salinity Meter: EM 6167      Calibration Check: 58.8      mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 21/4/05



### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 21/04/2005

Weather Condition: Sunny

Ambient Temperature °C: 25

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks			
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	a		b	Depth Average	
MW1 S		Stable	6	1	22.7	22.7	7.26	7.23	7.27	102.0	102.2	101.2	33.1	33.1	0.69	0.74	0.78	5	5	5.7		
MW1 M	11:05			3	21.1	21.1	7.31	7.28		100.3	100.4		33.0	33.0	0.93	0.88		5	4			
MW1 B				5	20.2	20.2	7.86	7.75		7.81	104.2		104.3	104.3	33.1	33.1		0.74	0.69		8	8
MW2 S		Stable	9	1	21.6	21.6	7.80	7.80	7.92	104.2	104.6	106.2	33.0	32.9	0.58	0.61	0.67	4	4	5.3		
MW2 M	10:55			4.5	20.2	20.2	8.06	8.01		107.5	108.3		33.0	33.0	0.65	0.60		5	5			
MW2 B				8	19.8	19.8	7.65	7.63		7.64	104.1		103.3	103.7	33.0	33.0		0.77	0.74		8	7
CW1 S		Stable	4	1	22.1	22.1	7.49	7.47	7.48	104.4	104.2	104.3	33.0	33.0	0.71	0.66	0.67	5	5	5.0		
CW1 M	11:10																					
CW1 B				3	20.9	20.9	7.09	7.11		7.10	88.1		96.3	91.2	33.1	33.1		0.62	0.67		4	6
CW2 S		Stable	10	1	22.4	22.4	7.47	7.39	7.78	105.1	104.9	106.4	33.1	33.1	0.60	0.60	0.70	8	8	5.8		
CW2 M	11:00			5	20.3	20.3	8.16	8.11		107.4	106.3		33.1	33.1	0.86	0.82		4	5			
CW2 B				9	19.7	19.7	7.65	7.59		7.62	106.0		103.8	104.9	33.1	33.2		0.71	0.63		5	5

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L OK 100% OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.08, 51.4, 503 NTU  
 Salinity Meter: EM 6157 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Anthony Ma

Checked By: [Signature]

Date: 23/4/05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 21/04/2005

Weather Condition: Sunny

Ambient Temperature: °C 27

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks	
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average		Depth Average		
MW1 S		Stable	6	1	23.2	23.3	7.31	7.30	7.66	106.6	105.6	105.4	33.2	33.2	0.26	0.20	0.87	5	5	5.0	
MW1 M	16.20			3	19.9	19.9	8.00	8.02		106.6	106.7		33.2	33.2	0.83	0.84		5	5		
MW1 B				5	19.8	19.8	7.66	7.71	7.69	99.7	100.4	103.1	33.4	33.4	1.61	1.50		5	5		
MW2 S		Stable	9	1	23.0	23.0	7.80	7.88	7.96	106.6	108.0	109.8	33.3	33.2	0.85	0.92	1.01	6	4	5.0	
MW2 M	16.00			4.5	20.1	20.1	8.17	8.00		112.4	112.0		33.1	33.1	1.00	1.02		4	5		
MW2 B				8	19.7	19.7	7.23	7.14	7.19	101.9	99.2	100.6	33.3	33.3	1.17	1.11		5	5		
CW1 S		Stable	4	1	23.1	23.1	7.74	7.77	7.76	108.2	109.0	108.6	33.2	33.2	0.98	1.00	1.00	5	6	5.5	
CW1 M	16.25																				
CW1 B				3	20.4	20.4	7.39	7.40	7.40	101.7	100.7	101.2	33.1	33.1	0.96	1.05		5	6		
CW2 S		Stable	10	1	22.2	22.2	7.48	7.35	8.01	110.0	108.1	111.4	33.2	33.2	0.47	0.57	1.03	5	7	5.0	
CW2 M	16.10			5	19.8	19.8	8.59	8.61		113.6	113.8		33.3	33.3	1.20	0.84		5	5		
CW2 B				9	19.6	19.6	7.44	7.45	7.45	99.1	99.0	99.1	33.4	33.4	1.53	1.54		4	4		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L OK 100% OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.08 51.4, 503 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6157

Sampled By: Anthony Ma

Checked By: AM

Date: 23/4/04

Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3  
 Date of Sampling: 23/04/2005 Weather Condition: Fine Ambient Temperature, °C: 26 Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L		Average	Dissolved Oxygen, %		Salinity, ppt		Turbidity, NTU		Average	Suspended Solids, mg/L		Depth Average	Remarks				
					a	b	a	b		a	b	a	b	a	b		a	b			a	b		
MW1 S		Stable	7	1	23.9	23.9	6.91	6.84	6.99	9.3	93.7	75.1	33.1	33.1	0.52	0.57	0.45	<3	<3	<3				
MW1 M	18:30			3.5	22.8	22.8	7.06	7.14		99.1	98.3		33.1	33.1	0.36	0.48		4	3					
MW1 B				6	21.8	21.8	7.21	7.30		7.26	93.0		93.6	93.3	33.2	33.1		0.40	0.39		<3	<2		
MW2 S		Stable	11	1	23.6	23.6	7.56	7.64	7.64	90.2	90.7	92.7	33.2	33.2	0.63	0.52	0.51	<3	3	<3				
MW2 M	18:00			5.5	22.7	22.7	7.66	7.71		90.8	91.0		33.1	33.2	0.43	0.45		<3	<3					
MW2 B				10	22.0	22.0	7.43	7.50		7.47	91.1		92.2	91.7	33.2	33.2		0.63	0.41		<3	<3		
CW1 S		Stable	5	1	23.7	23.7	6.77	6.83	6.80	94.0	95.2	93.6	33.3	33.2	0.49	0.59	0.58	<3	<3	<3				
CW1 M	18:45																							
CW1 B				4	22.9	22.9	7.25	7.33		7.29	96.6		97.3	97.0	33.3	33.3		0.68	0.54		3	3		
CW2 S		Stable	11	1	23.6	23.6	7.30	7.35	7.43	90.7	91.5	91.7	33.2	33.2	0.74	0.62	0.62	<3	<3	<3				
CW2 M	18:15			5.5	22.6	22.6	7.49	7.57		92.5	91.9		33.2	33.3	0.57	0.59		3	3					
CW2 B				10	21.9	21.9	7.51	7.54		7.53	94.0		94.6	94.3	33.1	33.2		0.68	0.52		<3	<3		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.11, 49.3, 498 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 25/4/05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No. 1618.3

Date of Sampling: 23/04/2005 Weather Condition: Cloudy Ambient Temperature, °C: 25 Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C			Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks
					a	b	Average	a	b	Average	a	b	Average	a	b	Average	Depth Average			
MW1 S		Stable	6	1	23.3	23.3	6.99	6.99	7.05	95.5	96.1	97.9	33.2	33.2	0.38	0.25	0.36	<3	<3	<3
MW1 M	12:05			3	21.8	21.8	7.12	7.11	100.9	99.0	99.0	33.2	33.2	0.22	0.24	<3	<3			
MW1 B				5	21.4	21.4	7.04	7.09	7.07	85.7	85.4	90.6	33.2	33.2	0.46	0.62	3	3		
MW2 S		Stable	10	1	22.3	22.3	7.31	7.25	7.37	102.6	102.4	102.1	33.1	33.1	0.42	0.40	0.51	<3	<3	<3
MW2 M	11:45			5	21.3	21.3	7.43	7.46	102.1	101.1	102.1	33.1	33.1	0.36	0.40	<3	<3			
MW2 B				9	20.8	20.8	7.59	7.53	7.50	102.5	102.6	102.6	33.2	33.2	0.70	0.75	<3	<3		
CW1 S		Stable	4	1	23.2	23.2	6.86	6.79	6.83	97.3	98.4	97.9	33.2	33.2	0.26	0.32	0.33	<3	<3	<3
CW1 M	12:10																	<3	<3	
CW1 B				3	21.3	21.3	8.28	8.02	8.15	109.8	114.6	112.2	33.2	33.2	0.33	0.40				
CW2 S		Stable	10	1	22.3	22.3	7.24	7.09	7.34	102.2	102.4	102.1	33.2	33.2	0.52	0.47	0.50	<3	<3	<3
CW2 M	11:55			5	21.2	21.2	7.50	7.52	7.52	102.0	101.9	102.0	33.2	33.2	0.42	0.47	<3	<3		
CW2 B				9	20.2	20.2	7.50	7.65	7.58	106.0	106.0	106.0	33.1	33.1	0.54	0.59	<3	<3		

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 5.11, 49.3, 498 NTU  
 Salinity Meter: EM 6157 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Chang  
 Checked By: [Signature]  
 Date: 25/4/05



## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 25/04/2005

Weather Condition: Rainy

Ambient Temperature, °C: 25

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C			Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Depth Average	Remarks
					a	b	Average	a	b	Average	a	b	Average	a	b	Average	a	b	Average	a		
MW1 S		Stable	6	1	22.7	22.7	6.25	6.35	7.05	88.0	91.4	97.7	33.2	33.2	0.83	0.77	0.98	6	7	5.7		
MW1 M	13:30			3	21.5	21.5	7.73	7.88		103.4	107.8		33.4	33.4	1.05	1.01		4	5			
MW1 B				5	21.3	21.3	7.00	7.01	7.01	92.1	92.0	92.1	33.2	33.2	1.08	1.12		7	8			
MW2 S		Stable	9	1	22.0	22.0	6.83	6.91	7.00	94.7	94.2	96.4	33.2	33.2	0.79	0.83	0.95	6	5	5.4		
MW2 M	13:00			4.5	21.5	21.5	7.20	7.04		98.3	98.4		33.3	33.3	1.39	1.34		5	5			
MW2 B				8	20.9	20.9	6.98	6.97	6.98	97.7	96.8	97.3	33.3	33.3	0.65	0.71		6	7			
CW1 S		Stable	4	1	22.7	22.7	6.18	6.24	6.21	83.6	84.4	84.0	33.2	33.2	0.87	0.95	0.92	5	5	6.1		
CW1 M	13:45																					
CW1 B				3	21.4	21.4	6.67	6.71	6.69	92.7	92.2	92.5	33.3	33.3	0.89	0.95		7	8			
CW2 S		Stable	10	1	22.2	22.2	6.48	6.53	6.88	87.8	88.3	94.1	33.2	33.2	0.59	0.64	0.97	7	7	5.6		
CW2 M	13:15			5	21.5	21.4	7.23	7.26		100.0	100.1		33.3	33.3	0.74	0.81		4	5			
CW2 B				9	20.9	20.9	6.90	6.91	6.91	92.4	92.7	92.6	33.4	33.4	1.50	1.56		5	6			

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK

Turbidity Meter: EM 2365 Calibration Check: 5.10, 49.5, 495 NTU

Salinity Meter: EM 6167 Calibration Check: 58.7 mS

Thermometer: EM 6187

Sampled By: Y.C. Cheng

Checked By: [Signature]

Date: 27.4.05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ke Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 27/04/2005

Weather Condition: Raining

Ambient Temperature: °C 24

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks				
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	Depth Average					
MW1 S		Stable	6	1	21.7	21.7	7.10	7.02	7.06	94.4	93.4	93.9	33.2	33.2	0.39	0.42	0.54	4	3	4.0			
MW1 M	06:40			3	21.3	21.3	7.10	7.03		94.4	93.5		33.4	33.4	0.50	0.48		5	4				
MW1 B				5	21.3	21.3	7.00	6.89		6.95	93.1		91.6	92.4	33.4	33.4		0.67	0.77		4	4	
MW2 S		Stable	10	1	21.8	21.8	7.18	7.15	7.04	95.5	95.1	93.7	33.3	33.3	0.55	0.48	0.49	3	3	3.9			
MW2 M	06:15			5	21.3	21.3	6.89	6.95		91.6	92.4		33.4	33.4	0.54	0.43		4	4				
MW2 B				9	20.9	20.9	6.95	6.93		6.94	90.7		90.4	90.6	33.2	33.4		0.46	0.47		5	5	
CW1 S		Stable	4	1	21.8	21.8	7.10	7.15	7.13	94.4	95.1	94.8	33.3	33.3	0.45	0.41	0.49	4	3	3.8			
CW1 M	06:30																						
CW1 B				3	21.4	21.4	6.90	6.95		6.93	91.8		92.4	92.1	33.4	33.4		0.61	0.49		4	5	
CW2 S		Stable	10	1	21.7	21.7	7.01	7.05	6.96	93.2	93.6	92.6	33.3	33.3	0.55	0.46	0.54	5	6	5.0			
CW2 M	06:35			5	21.2	21.3	6.89	6.90		91.6	91.8		33.4	33.4	0.66	0.56		4	4				
CW2 B				9	21.1	21.1	6.90	6.98		6.94	91.8		91.8	91.8	33.4	33.4		0.52	0.45		7	5	

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 4.98, 49.2, 489 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: *[Signature]*  
 Date: 29.4.05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 27/04/2005

Weather Condition: Raining

Ambient Temperature, °C: 25

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU			Suspended Solids, mg/L		Remarks		
					a	b	a	b	Average	a	b	Average	a	b	a	b	Average	Depth	Average			
MW1 S	13:30	Stable	6	1	21.8	21.6	7.05	7.02	7.01	93.8	93.4	93.3	33.2	33.2	0.89	0.80	0.70	4	5	4.5		
MW1 M				3	21.6	21.6	7.01	6.97		93.2	92.7		33.4	33.4	0.51	0.63		6	5			
MW1 B				5	21.4	21.4	6.99	6.94		93.0	92.3		92.6	33.4	33.5	0.72		0.67	4			4
MW2 S	13:00	Stable	9	1	21.6	21.7	6.94	7.05	6.97	92.3	93.6	92.7	33.3	33.3	0.45	0.46	0.51	5	6	5.4		
MW2 M				4.5	21.3	21.3	6.95	6.93		92.4	92.2		33.5	33.5	0.49	0.60		6	6			
MW2 B				8	21.1	21.1	6.95	6.95		92.4	92.4		92.4	33.5	33.5	0.59		0.49	6			6
CW1 S	13:45	Stable	4	1	21.7	21.7	6.94	6.93	6.94	92.3	92.2	92.2	33.3	33.3	0.64	0.57	0.67	4	5	4.6		
CW1 M																						
CW1 B				3	21.7	21.7	6.95	6.95		92.4	92.4		92.4	33.5	33.5	0.65		0.80	6			5
CW2 S	13:15	Stable	10	1	21.4	21.6	6.98	6.95	6.87	92.4	92.5	91.2	33.3	33.3	0.72	0.66	0.61	5	5	5.9		
CW2 M				5	21.6	21.6	6.82	6.72		90.7	89.4		33.5	33.5	0.58	0.62		7	8			
CW2 B				9	21.2	21.1	6.84	6.86		91.0	91.2		91.1	33.4	33.4	0.50		0.55	6			5

Equipment used: Dissolved Oxygen Meter EM 6167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 4.98, 49.2, 469 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 29.4.05



Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 27/04/2005

Weather Condition: Raining

Ambient Temperature, °C: 24

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L		Average	Dissolved Oxygen, %		Salinity, ppt		Turbidity, NTU		Average	Suspended Solids, mg/L		Depth Average	Remarks	
					a	b	a	b		a	b	a	b	a	b		a	b			
MK1 S		Stable	7	1	21.7	21.7	7.09	7.09	7.20	94.3	94.3	95.8	33.3	33.2	0.38	0.46	0.55	5	4	5.5	
MK1 M	07:30			3.5	21.7	21.7	7.34	7.29	97.6	97.0	92.2	92.7	92.4	33.5	33.5	0.56	0.68	6	7		
MK1 B				6	21.4	21.3	6.93	6.97	6.95	92.2	92.7	92.4	33.5	33.5	0.56	0.68	6	6			
MK2 S		Stable	16	1	21.7	21.7	7.37	7.36	7.37	98.0	97.9	98.0	33.3	33.3	0.43	0.42	0.57	5	5	5.2	
MK2 M	07:45			8	21.2	21.2	7.37	7.36	98.0	97.9	98.0	97.9	98.0	33.5	33.5	0.54	0.53	5	6		
MK2 B				15	21.0	21.0	7.19	7.12	7.16	95.6	94.7	95.2	33.5	33.5	0.70	0.80	6	5			
MK3 S		Stable	8	1	21.7	21.7	7.19	7.15	6.99	95.6	95.1	92.9	33.2	33.3	0.49	0.43	0.49	6	6	6.3	
MK3 M	07:00			4	21.6	21.6	6.80	6.80	6.80	90.4	90.4	90.6	47.5	47.5	0.54	0.52	7	6			
MK3 B				7	21.0	21.0	6.80	6.82	6.81	90.4	90.7	90.6	47.1	47.1	0.45	0.51	7	7			
MK4 S		Stable	15	1	21.7	21.7	7.01	7.02	7.05	93.2	93.4	93.8	47.5	47.5	0.41	0.43	0.47	6	6	6.4	
MK4 M	07:15			7.5	21.3	21.3	7.12	7.06	7.06	94.7	93.9	94.5	47.3	47.5	0.38	0.36	5	5			
MK4 B				14	21.1	21.1	7.12	7.09	7.11	94.7	94.3	94.5	33.5	33.5	0.58	0.64	9	8			
CK1 S		Stable	17	1	21.7	21.7	7.11	7.13	7.06	94.8	94.8	93.9	33.4	33.4	0.41	0.42	0.44	8	6	6.2	
CK1 M	08:00			8.5	21.6	21.6	6.99	7.00	7.00	93.0	93.1	93.9	33.4	33.4	0.41	0.41	6	5			
CK1 B				16	20.7	20.6	6.93	6.89	6.91	92.2	91.6	91.9	33.5	33.5	0.52	0.46	7	5			
CK2 S		Stable	20	1	21.6	21.6	6.85	6.80	6.83	91.1	90.4	90.8	33.4	33.4	0.46	0.42	0.47	8	6	6.3	
CK2 M	07:50			10	21.4	21.4	6.84	6.82	6.83	91.0	90.7	90.8	33.5	33.5	0.42	0.44	6	5			
CK2 B				19	20.3	20.3	6.72	6.73	6.73	89.4	89.5	89.4	33.6	33.6	0.54	0.55	5	7			

Equipment used: Dissolved Oxygen Meter: EM 6167  
 Turbidity Meter: EM 2365  
 Salinity Meter: EM 6167  
 Thermometer: EM 6167

EM 6167  
 EM 2365  
 EM 6167  
 EM 6167

Calibration Check: 0mg/L: OK 100% OK  
 Calibration Check: 4.98, 49.2, 489 NTU  
 Calibration Check: 58.7 mS

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 27.4.05

Water Quality Monitoring Data Sheet (Ko Lau Wan)



Project: Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd.

Job No.: 1618.3

Date of Sampling: 27/04/2005

Weather Condition: Raining

Ambient Temperature, °C: 24

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L		Average	Dissolved Oxygen, %		Salinity, ppt		Turbidity, NTU		Average	Suspended Solids, mg/L		Depth Average	Remarks	
					a	b	a	b		a	b	a	b	a	b		a	b			a
MK1 S		Stable	5	1	21.6	21.6	7.09	7.11	7.06	94.3	94.6	93.8	33.3	33.3	0.45	0.44	0.53	5	5	4.8	
MK1 M	14:30			3	21.5	21.4	7.05	6.97		93.8	92.7		33.4	33.5	0.60	0.71		5	4		
MK1 B				5	21.3	21.3	7.25	7.16		7.21	96.4		95.2	95.8	33.5	33.5		0.46	0.52		5
MK2 S		Stable	15	1	21.5	21.5	7.54	7.51	7.34	100.3	99.9	97.6	33.5	33.5	0.63	0.58	0.61	7	7	5.6	
MK2 M	14:45			7.5	21.3	21.2	7.13	7.18		94.8	95.5		33.5	33.5	0.64	0.69		4	5		
MK2 B				14	21.0	21.0	6.54	6.52		6.53	87.0		86.7	86.8	33.5	33.5		0.63	0.50		6
MK3 S		Stable	6	1	21.7	21.7	7.35	7.37	7.30	97.8	98.0	97.1	3.3	33.3	0.59	0.67	0.56	5	5	4.9	
MK3 M	14:00			3	21.4	21.5	7.28	7.20		96.8	95.8		33.5	33.5	0.40	0.47		4	4		
MK3 B				5	21.0	21.0	7.32	7.45		7.39	97.4		99.1	98.2	33.5	33.5		0.58	0.67		6
MK4 S		Stable	13	1	21.6	21.6	7.17	7.21	7.37	95.4	95.9	98.0	33.4	33.4	0.56	0.49	0.59	4	4	5.8	
MK4 M	14:15			6.5	21.5	21.4	7.52	7.57		100.0	100.7		33.5	33.5	0.51	0.58		7	6		
MK4 B				12	21.3	21.3	7.15	7.21		7.18	95.1		95.9	95.5	3.5	33.5		0.64	0.75		7
CK1 S		Stable	15	1	21.6	21.7	7.48	7.49	7.43	99.5	99.6	98.8	33.4	33.4	0.45	0.52	0.54	5	5	5.2	
CK1 M	15:15			7.5	21.5	21.5	7.36	7.38		97.9	98.2		33.5	33.5	0.69	0.56		7	5		
CK1 B				14	21.3	21.2	6.75	6.73		6.74	89.8		89.5	89.6	33.4	33.5		0.50	0.51		5
CK2 S		Stable	19	1	21.6	21.6	7.62	7.60	7.57	101.3	101.1	100.6	33.4	33.4	0.65	0.64	0.55	5	5	5.0	
CK2 M	15:00			9.5	21.5	21.5	7.52	7.52		100.0	100.0		33.5	33.5	0.50	0.40		6	6		
CK2 B				18	20.1	20.1	6.45	6.43		6.44	85.8		85.5	85.7	33.6	33.6		0.56	0.54		7

Equipment used: Dissolved Oxygen Meter: EM 6167 Calibration Check: 0mg/L OK 100% OK  
 Turbidity Meter: EM 2365 Calibration Check: 4.98, 49.2, 489 NTU  
 Salinity Meter: EM 6167 Calibration Check: 58.7 mS  
 Thermometer: EM 6167

Sampled By: Y.C. Cheng  
 Checked By: [Signature]  
 Date: 29.4.05

### Water Quality Monitoring Data Sheet (Wong Shek)



Project Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client Kin Shing Construction Co., Ltd. Job No. 1618.3

Date of Sampling: 29/04/2005

Weather Condition: Cloudy

Ambient Temperature: 22 °C

Tide State: Mid-Flood

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/l		Depth Average	Remarks		
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average				
MW1 S		Small Wave	7	1	21.9	21.9	7.82	7.77	7.74	90.1	90.4	90.0	32.0	32.1	1.02	1.07	1.02	<3	<3	<3		
MW1 M	08:00			3.5	21.2	21.2	7.72	7.63				89.8	89.6		32.0	32.0	0.98	0.94				
MW1 B				6	20.8	20.7	7.52	7.55	7.54			88.4	88.8	88.6	32.0	32.1	1.05	1.07		4	4	
MW2 S		Small Wave	10	1	21.9	22.0	7.25	7.33	7.24	89.5	89.1	88.3	32.0	32.1	1.02	1.02	1.06	3	3	<3		
MW2 M	07:00			5	21.4	21.4	7.16	7.22				87.0	87.6		32.1	32.1	1.13	1.15				
MW2 B				9	21.0	20.9	7.07	7.10	7.09			86.4	86.9	86.7	32.0	32.0	0.99	1.04		3	3	
CW1 S		Small Wave	5	1	21.6	21.7	7.40	7.44	7.42	85.0	85.8	85.4	32.0	32.0	1.18	1.20	1.20	<3	<3	3.3		
CW1 M	07:40																					
CW1 B				4	21.4	21.4	7.20	7.25	7.23			82.5	83.1	82.8	31.9	31.9	1.22	1.19		5	5	
CW2 S		Small Wave	11	1	22.0	22.0	7.37	7.42	7.30	84.1	83.6	83.1	32.0	32.1	0.99	0.94	1.11	<3	<3	<3		
CW2 M	07:20			5.5	21.2	21.3	7.18	7.23				82.5	82.2		32.0	32.0	1.25	1.23		3	4	
CW2 B				10	20.7	20.8	7.08	7.11	7.09			80.9	81.1	81.0	32.1	32.0	1.10	1.13		<3	3	

Equipment used: Dissolved Oxygen Meter: EM 5167 Calibration Check: 0mg/L: OK 100%: OK  
 Turbidity Meter: EM 2365 Calibration Check: 4.95, 49.0, 495 NTU  
 Salinity Meter: EM 5157 Calibration Check: 58.7 mS  
 Thermometer: EM 5167

Sampled By: Daniel  
 Checked By: *[Signature]*  
 Date: 31.4.05

## Water Quality Monitoring Data Sheet (Wong Shek)



Project: Contract No. CV2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public Piers

Client: Kin Shing Construction Co., Ltd. Job No.: 1618.3

Date of Sampling: 29/04/2005

Weather Condition: Sunny

Ambient Temperature, °C: 26

Tide State: Mid-Ebb

Station	Time	Sea Condition	Overall Depth, m	Sampling Depth, m	Temperature, °C		Dissolved Oxygen, mg/L			Dissolved Oxygen, %			Salinity, ppt		Turbidity, NTU		Suspended Solids, mg/L		Remarks	
					a	b	a	b	Average	a	b	Average	a	b	Average	a	b	Average		Depth
MW1 S		Small Wave	6	1	23.1	23.0	7.14	7.20	7.13	88.1	88.8	87.8	33.1	33.1	0.92	0.94	4	4	3.2	
MW1 M	15:50			3	22.5	22.4	7.06	7.10	7.02	86.9	87.4	86.7	33.1	33.0	1.06	1.11	1.07	<3		3
MW1 B				5	21.9	22.0	7.01	7.02	7.02	83.2	83.6	83.4	33.1	33.2	1.17	1.20	1.12	3		<3
MW2 S		Small Wave	9	1	23.2	23.2	7.28	7.33	7.27	87.5	88.1	86.7	33.0	33.0	0.90	0.91	4	4	<3	
MW2 M	14:37			4.5	22.5	22.5	7.20	7.25	7.22	86.0	85.2	85.6	33.1	33.1	1.17	1.20	1.11	<3		<3
MW2 B				8	22.0	22.0	7.06	7.11	7.09	84.9	84.3	84.6	33.2	33.2	1.25	1.24	1.24	<3		3
CW1 S		Small Wave	4	1	23.1	23.1	7.31	7.34	7.33	85.1	84.4	84.8	33.2	33.2	1.06	1.09	3	4	3.8	
CW1 M	15:22																			
CW1 B				3	22.5	22.6	7.20	7.17	7.19	83.4	82.9	83.2	33.1	33.2	1.15	1.18	1.12	4		4
CW2 S		Small Wave	10	1	23.0	23.0	7.25	7.34	7.21	88.2	88.5	88.9	33.0	33.0	0.94	0.99	4	4	3.8	
CW2 M	15:00			5	22.4	22.5	7.11	7.12	7.11	89.2	89.8	89.5	33.0	33.0	1.08	1.08	1.08	4		3
CW2 B				9	21.9	21.8	7.01	6.99	7.00	86.3	85.9	86.1	33.2	33.2	1.15	1.23	1.19	4		5

Equipment used: Dissolved Oxygen Meter: EM 6167  
 Turbidity Meter: EM 2365  
 Salinity Meter: EM 6167  
 Thermometer: EM 6167

Calibration Check: 0mg/L OK 100% OK  
 Calibration Check: 4.95, 49.0, 495 NTU  
 Calibration Check: 58.7 mS

Sampled By: Daniel  
 Checked By:   
 Date: 31.4.05

## Quality Assurance Report on laboratory tests

### Determination of suspended solids

Date of Analysis	Blank		Quality Control		Duplicate Analysis		Spike Recovery Analysis	
	Acceptable Range g	Analysis Results g	Acceptable Range mg/L	Analysis Results mg/L	Acceptable Range %	Analysis Results %	Acceptable Range %	Analysis Results %
04/04/2005	-0.0003 to 0.0003	0.0000 to 0.0001	43 to 55	48 to 52	less than 15	0 to 8	78 to 114	95 to 105
06/04/2005	-0.0003 to 0.0003	0.0000 to 0.0001	43 to 55	48 to 53	less than 15	0 to 15	78 to 114	98 to 103
08/04/2005	-0.0003 to 0.0003	0.0000 to 0.0001	43 to 55	50 to 51	less than 15	0 to 8	78 to 114	95 to 100
11/04/2005	-0.0003 to 0.0003	0.0000 to 0.0002	43 to 55	49 to 50	less than 15	0 to 7	78 to 114	101 to 105
19/04/2005	-0.0003 to 0.0003	0.0000 to 0.0002	43 to 55	49 to 52	less than 15	0 to 8	78 to 114	100 to 103
21/04/2005	-0.0003 to 0.0003	0.0001 to 0.0002	43 to 55	50 to 51	less than 15	0 to 2	78 to 114	95 to 102
23/04/2005	-0.0003 to 0.0003	0.0000 to 0.0003	43 to 55	49 to 52	less than 15	10 to 11	78 to 114	102 to 105
25/04/2005	-0.0003 to 0.0003	-0.0001 to 0.0002	43 to 55	49 to 52	less than 15	0 to 5	78 to 114	100 to 102
27/04/2005	-0.0003 to 0.0003	-0.0001 to 0.0003	43 to 55	48 to 52	less than 15	4 to 6	78 to 114	98 to 103
29/04/2005	-0.0003 to 0.0003	-0.0001 to 0.0003	43 to 55	49 to 51	less than 15	4 to 7	78 to 114	93 to 95

\*Limit of Detection:1mg/L

**APPENDIX VI**  
**COMPLAINT LOG**



**APPENDIX VII**

**Cumulative Statistics on Complaints, Notifications of Summonses and Successful Prosecutions**



<b>Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public</b>			
<b>Cumulative Statistics on Complaints</b>			
Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Month	Cumulative Number to Date
Air	-	-	-
Noise	-	-	-
Water	-	-	-
Waste	-	-	-
<b>Total</b>	<b>-</b>	<b>-</b>	<b>-</b>

<b>Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public</b>			
<b>Cumulative Statistics on Successful Prosecutions</b>			
Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative Number to Date
Air	-	-	-
Noise	-	-	-
Water	-	-	-
Waste	-	-	-
<b>Total</b>	<b>-</b>	<b>-</b>	<b>-</b>

<b>Contract No. CV/2004/02 Reconstruction of Wong Shek and Ko Lau Wan Public</b>			
<b>Cumulative Statistics on Notification of Summons</b>			
Environmental Parameters	Cumulative No. Brought Forward	No. of Notification of Summons	Cumulative Number to Date
Air	-	-	-
Noise	-	-	-
Water	-	-	-
Waste	-	-	-
<b>Total</b>	<b>-</b>	<b>-</b>	<b>-</b>

**APPENDIX VIII**

**Monitoring Schedule for Next Month**

**CEDD Contract No. CV/2004/02**  
**Reconstruction of Wong Shek and Ko Lau Wan Public Piers**  
**Water Quality Monitoring Schedule**  
**May 2005**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3 WQM <sup>3</sup> (Ebb: 08:35) (Flood: 13:48)	4	5 WQM <sup>1</sup> (Ebb: 10:18) (Flood: 16:16)	6	7 WQM <sup>1</sup> (Ebb: 11:49) (Flood: 17:30)
8	9 WQM <sup>1</sup> (Ebb: 13:08) (Flood: 07:35)	10	11 WQM <sup>3</sup> (Ebb: 12:50) (Flood: 06:47)	12	13 WQM <sup>1</sup> (Ebb: 14:12) (Flood: 07:45)	14
15	16	17 WQM <sup>3</sup> (Flood: 08:25)	18	19 WQM <sup>1</sup> (Ebb: 09:32) (Flood: 14:52)	20	21 WQM <sup>1</sup> (Ebb: 10:42) (Flood: 17:02)
22	23 WQM <sup>1</sup> (Ebb: 11:59) (Flood: 18:00)	24	25 WQM <sup>1</sup> (Ebb: 13:28) (Flood: 07:31)	26	27 WQM <sup>3</sup> (Ebb: 15:08) (Flood: 07:38)	28
29	30 WQM <sup>3</sup> (Ebb: 17:03) (Flood: 10:28)	31				

Notes:

1. WQM - water quality monitoring on mid-flood and mid-ebb tides at Wong Shek (CW1, CW2, MW1 & MW2)
2. WQM - water quality monitoring on mid-flood and mid-ebb tides at Ko Lau Wan (CK1, CK2, MK1, MK2, MK3 & MK4)
3. WQM - water quality monitoring on mid-flood and mid-ebb tides at Ko Lau (CK1, CK2, MK1, MK2, MK3 & MK4) and Wong Shek (CW1, CW2, MW1 & MW2)

**APPENDIX IX**


**Master Construction Programme**

Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lan Wan Public Piers

### Master Programme (Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

No.	Task Name	Duration	Start	Finish	Predecessors
1	Commencement of the Works	1 day	Mon 04/11/05	Mon 04/11/05	
2	Completion of Section 1 (Wong Shek Public Pier)	1 day	Sun 06/08/06	Sun 06/08/06	
3	Completion of Section 2 (Ko Lan Wan Public Pier)	1 day	Sun 06/08/06	Sun 06/08/06	
4	Preliminary				
5	Establishment of Engineer's Principal Site Office	994 days	Tue 04/11/04	Mon 07/08/06	
6	Submission and approval	21 days	Tue 04/11/04	Mon 04/12/04	
7	Provision	8 days	Tue 04/12/04	Tue 04/12/04	
8	Servicing during construction period	600 days	Wed 04/12/05	Sun 06/08/06	
9	Servicing during maintenance period	364 days	Mon 06/08/07	Sun 07/03/05	
10	Decommissioning	1 day	Mon 07/08/06	Mon 07/08/06	
11	Secondary Office	582 days	Mon 05/1/05	Mon 06/08/07	
12	Submission and approval	15 days	Mon 05/01/05	Mon 05/17/05	
13	Provision	28 days	Tue 05/01/05	Mon 05/23/05	
14	Servicing	538 days	Tue 05/02/05	Sun 06/08/06	
15	Decommissioning	1 day	Mon 06/08/07	Mon 06/08/07	
16	Provision of Contractor's accommodation	602 days	Mon 04/12/03	Sun 06/08/06	
17	Initial survey	20 days	Wed 04/12/05	Mon 05/01/05	
18	Erection of hoarding and project signboard at Pier A	34 days	Mon 05/01/05	Sat 05/07/05	
19	Erection of hoarding and project signboard at Pier B	13 days	Mon 05/02/05	Sat 05/07/05	
20	Application and installation of electrical system	75 days	Fri 04/12/05	Tue 05/03/05	
21	Application and installation of water supply system	75 days	Sun 05/01/05	Thu 05/05/05	
22	Application and installation of telephone lines	75 days	Sun 05/01/05	Thu 05/05/05	
23	Notification of parties in concern	34 days	Wed 04/12/04	Fri 04/12/05	
24	Application for promulgation of Marine Department Notice for Wong Shek	71 days	Fri 04/12/04	Fri 05/02/05	
25	Application for promulgation of Marine Department Notice for Ko Lan Wan	65 days	Fri 04/12/04	Sat 05/02/05	
26	Environmental Monitoring	658 days	Mon 04/11/05	Sun 06/09/03	
27	Submission and approval of ES and IC (Env)	44 days	Mon 04/11/05	Tue 04/12/05	
28	Endorsement of tM&A proposal	12 days	Wed 04/12/05	Sun 05/01/05	
29	Baseline water quality monitoring	26 days	Mon 05/01/05	Fri 05/06/05	
30	Preparation and approval of baseline report	21 days	Sat 05/02/05	Fri 05/06/05	
31	Impact monitoring	527 days	Sat 05/02/06	Sun 06/08/06	
32	Post-construction monitoring	28 days	Mon 06/08/07	Sun 06/09/03	
33	Section 1 (Wong Shek Public Pier)				
34	Temporary cover to existing pier	121 days	Mon 04/11/05	Tue 05/03/05	
35	Design and ICE checking	66 days	Mon 04/11/05	Wed 05/11/05	

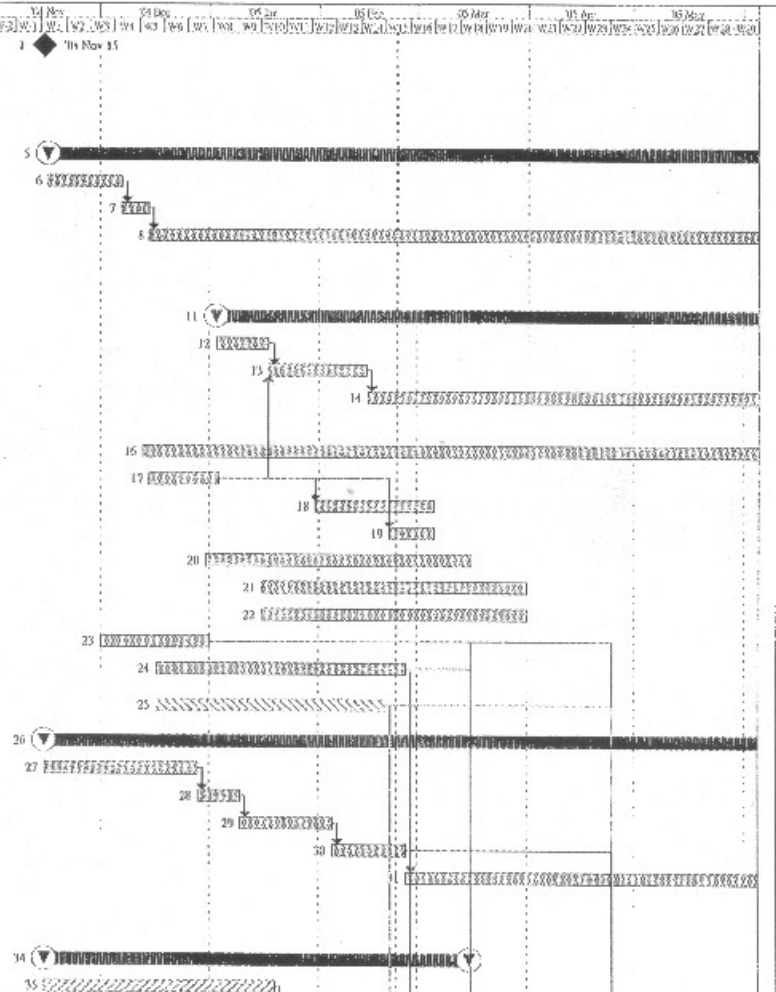

Drawn by: P.2004/022  
 Master Programme (Ver 2.0)

Round Task: Progress: Summary: Critical Task (Sec 1 & 2): Critical Task (Sec 1): Maintenance Period:

Split: Commencement Milestone: Completion Milestone:

2005.11.23.17:00

#2663 P.002 /013


Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

### Master Programme (Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

FEB-23-2005 17:01

ID	Task Name	Duration	Start	Finish	Resources
35	Submission for Engineer's comment	30 days	Thu 05/1/20	Fri 05/2/18	35
36	Erection	20 days	Sat 05/2/19	Thu 05/3/10	36
37	Certified by ICE and commissioning	5 days	Fri 05/3/11	Tue 05/3/15	37
38	Provision of temporary berth	192 days	Mon 04/11/15	Wed 05/5/25	
39	Design and ICE checking of temporary berth	80 days	Mon 04/11/15	Wed 05/2/22	
40	Submission for Engineer's comment	41 days	Thu 05/2/3	Tue 05/3/15	40
41	Piling	40 days	Wed 05/3/16	Sun 05/4/24	34,36,37,41,38
42	Deck construction and installation of fenders	25 days	Mon 05/4/25	Thu 05/5/19	42
43	Relocation of navigation light by Marine Dept.	66 days	Wed 05/3/16	Fri 05/5/20	
44	Application to Marine Department	65 days	Wed 05/3/16	Thu 05/5/19	
45	Relocation works	1 day	Fri 05/5/20	Fri 05/5/20	45,43
46	Certified by ICE, testing and commissioning of berth	5 days	Sat 05/5/21	Wed 05/5/25	46
47	Ground Investigation	110 days	Wed 04/12/29	Sun 05/4/07	
48	Submission for Engineer's comment	59 days	Wed 04/12/29	Fri 05/2/25	
49	Ground investigation works on site	20 days	Sat 05/2/26	Thu 05/3/17	49,34,36
50	Preparation and approval of reports	10 days	Fri 05/3/18	Sun 05/3/27	50
51	Submission of reports and determine pile founding levels	21 days	Mon 05/3/28	Sun 05/4/17	51
52	Piling for permanent pier	282 days	Sat 05/1/1	Sun 05/10/9	
53	Compilation of method statement for piling	33 days	Sat 05/1/1	Wed 05/2/2	
54	Submission for Engineer's comment	112 days	Thu 05/2/3	Wed 05/5/25	54
55	Vertical preliminary pile and testing	15 days	Thu 05/5/26	Thu 05/6/9	47,52,53,127
56	Vertical main piles using land plant (B1, H1, E2, H2)	30 days	Tue 05/6/28	Wed 05/7/27	
57	Vertical main piles (A11, B8, B11, C8, C11, D8, D11)	18 days	Sun 05/6/19	Wed 05/7/6	128
58	Temporary platform for raking pile	21 days	Thu 05/7/7	Wed 05/7/27	13
59	Vertical main piles (remaining 14 nos.)	35 days	Thu 05/7/7	Wed 05/8/10	14
60	Raking preliminary piles and testing (B10)	15 days	Thu 05/7/28	Thu 05/8/11	59,56
61	Raking main piles (15 nos)	44 days	Fri 05/8/12	Sat 05/9/24	61
62	Pile test for main piles	15 days	Sun 05/9/25	Sun 05/10/9	62
63	Construction of pile cap and deck	212 days	Fri 05/6/10	Sat 06/1/7	
64	Submission and approval of precast yard	61 days	Fri 05/6/10	Thu 05/8/9	
65	Casting of precast units at precast yard	61 days	Wed 05/8/10	Sun 05/10/9	65
66	Design and ICE checking of falsework for pile cap and deck construction	62 days	Sun 05/7/10	Fri 05/9/9	
67	Submission of calculation and method statement for Engineer's approval	30 days	Sat 05/9/10	Sat 05/10/9	67
68	Erection of falsework for installation of precast units	20 days	Mon 05/10/10	Sat 05/10/29	68,61

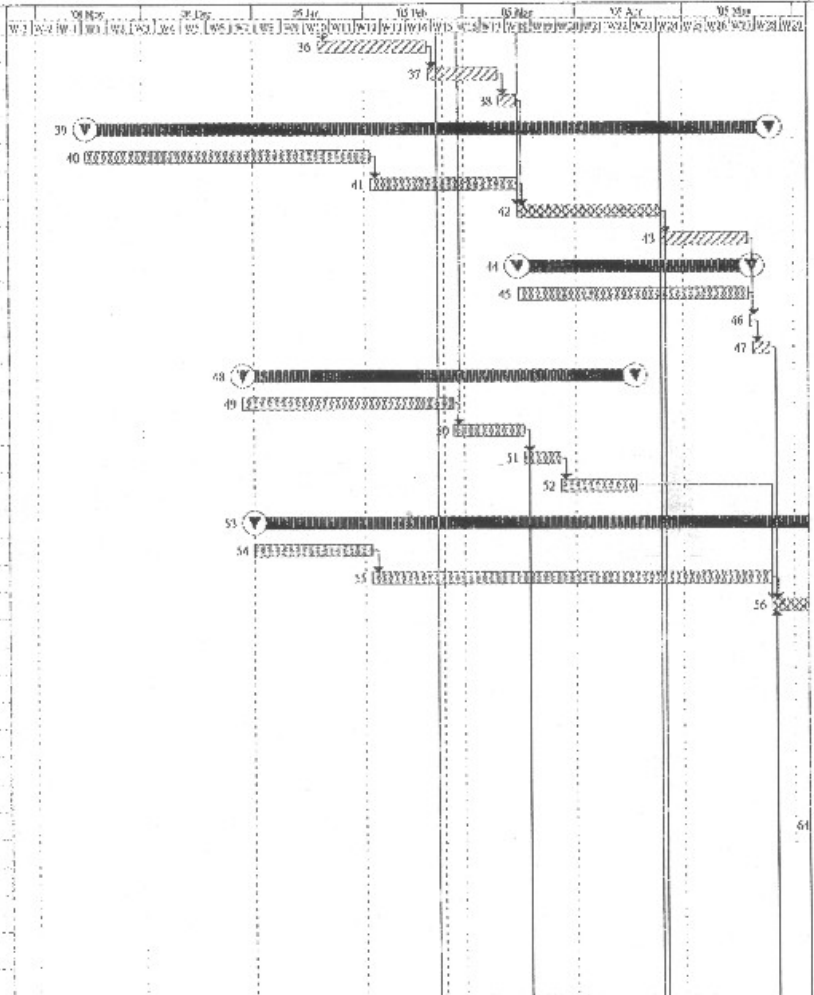

#2563 P.003 /013

Version No: CV/2004/02  
 Master Programme (Version 2)

Name: Task (33333333333333)    Progress: ██████████    Status: Critical Task (Sec 1 & 2) Critical Task (Sec 2)

Split: .....    Commencement Milestone: ◆    Completion Milestone: ★    Critical Task (Sec 1) Maintenance Period

Page 2

Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme (Version 2)


Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

Sl. No.	Task Name	Duration	Start	Finish	Predecessors	16 Nov	17 Dec	18 Jan	19 Feb	20 Mar	21 Apr	22 May	23 Jun	24 Jul	25 Aug
00	Installation of precast girders with in-situ pile caps	60 days	Mon 05/10/04	Thu 05/12/04	44,48,53										
01	Casting of in-situ pier deck	30 days	Fri 05/12/04	Sat 06/1/05	46,78										
02	Construction of bollards	30 days	Fri 05/12/04	Sat 06/1/05	70										
03	Installation of corrosion monitoring system	91 days	Sun 05/10/04	Sat 06/1/05											
04	Approval of specialist contractor and method statement	61 days	Sun 05/10/04	Thu 05/12/04											
05	Installation of corrosion monitoring system	30 days	Fri 05/12/04	Sat 06/1/05	78,74										
06	Roof cover systems	272 days	Tue 05/8/04	Sun 06/5/07											
07	Approval of specialist contractor	61 days	Tue 05/8/04	Sat 05/30/04											
08	Submission of workshop drawings for connection details with deck	61 days	Sun 05/10/04	Thu 05/12/04	79										
09	Material submissions	91 days	Sun 05/10/04	Sat 06/1/05	79										
10	Submission of workshop drawing for remaining roof system	91 days	Sun 05/10/04	Sat 06/1/05	79										
11	Construction of steel works	60 days	Sun 06/1/05	Wed 06/3/05	71,80,75										
12	Erection of roof covers	60 days	Thu 06/3/05	Sun 06/5/07	81										
13	Marrying-in to landside	121 days	Wed 06/3/05	Thu 06/7/05											
14	Application of Excavation Permit	90 days	Wed 06/3/05	Mon 06/6/05											
15	Site works	31 days	Tue 06/6/05	Thu 06/7/05	81,82										
16	Electrical system, CLP meter box and lighting system	220 days	Mon 05/10/04	Wed 06/5/17											
17	Approval of specialist contractor	30 days	Mon 05/10/04	Tue 05/11/04											
18	Liaison with CLP and EMSD	60 days	Wed 05/11/04	Sat 06/1/05	87										
19	Installation	120 days	Sun 06/1/05	Sun 06/5/07	71,88										
20	Testing	10 days	Mon 06/5/05	Wed 06/5/17	89										
21	Construction of floor finish	121 days	Wed 06/3/05	Thu 06/7/05											
22	Material submissions	61 days	Wed 06/3/05	Sun 06/5/07											
23	Site works	60 days	Mon 06/5/05	Thu 06/7/05	82,92										
24	Construction of hand railing, seating benches and notice boards	150 days	Tue 06/2/07	Thu 06/7/06											
25	Material submission	60 days	Tue 06/2/07	Fri 06/4/07											
26	Construction	90 days	Sat 06/4/08	Thu 06/7/06	81,93										
27	Installation of fender system	190 days	Thu 05/12/04	Thu 06/7/06											
28	Material submission	31 days	Thu 05/12/04	Sat 06/1/05											
29	Ordering of material	59 days	Sun 06/1/05	Tue 06/5/07	90										
30	Site works	100 days	Wed 06/5/05	Thu 06/7/05	71,91										
31	Relocation of navigation light by Marine Dept.	92 days	Fri 06/4/07	Fri 06/7/07											
32	Application to Marine Department	91 days	Fri 06/4/07	Thu 06/7/06											

3EB9-23-2005 17:01 #2663 P.004 /013

Contract No.: CV/2004/02  
 Master Programme (Version 2)

General Task



Program



Summary



Critical Task (Sec 1 & 2)



Critical Task (Sec 2)



Split



Constraint Task Milestone

Completion Milestone

Critical Task (Sec 1)



Maintenance Period




Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

### Master Programme (Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

Sl. No.	Task Name	Duration	Start	Finish	Professional
11	Relocation	1 day	Fri 06/7/7	Fri 06/7/7	105,955,951,109,96
12	Commissioning of the pier	1 day	Sat 06/7/8	Sat 06/7/8	103
105	Demolition of the temporary berth and the existing pier	151 days	Thu 06/3/9	Sun 06/8/6	
105	Survey of existing structures	31 days	Thu 06/3/9	Sat 06/4/8	
107	Design and ICE checking of demolition plan	61 days	Sun 06/4/9	Thu 06/6/8	106
108	Submission for Engineer's comments	30 days	Fri 06/6/9	Sat 06/7/8	107
109	Obtain consent from Country and Marine Park Authority	30 days	Fri 06/6/9	Sat 06/7/8	107
111	Demolition	29 days	Sun 06/7/9	Sun 06/8/6	104,109,109
111	Maintenance Period for the Works	365 days	Mon 06/8/7	Mon 07/8/6	110
<b>Section 2 (Ko Lau Wan Public Pier)</b>					
115	Current Survey	626 days	Mon 04/11/15	Wed 06/8/2	
116	Submission and approval of specialist and method statement	75 days	Mon 04/11/15	Wed 05/1/26	
117	Initial coral survey and approval by APCD	18 days	Sun 05/2/20	Wed 05/3/9	114,25
118	Coral translocation	4 days	Thu 05/3/10	Sun 05/3/13	115
117	Post translocation survey	4 days	Mon 05/3/14	Thu 05/3/17	116
118	Post pier construction survey	15 days	Wed 06/7/19	Wed 06/8/2	107
119	Temporary cover to existing pier	123 days	Mon 04/11/15	Thu 05/3/07	
120	Design and ICE checking	66 days	Mon 04/11/15	Wed 05/1/19	
121	Submission for Engineer's comment	30 days	Thu 05/1/20	Fri 05/2/18	120
122	Direction	22 days	Sat 05/2/19	Sat 05/3/12	121
123	Certified by ICE and commissioning	5 days	Sun 05/3/13	Thu 05/3/17	122
124	Provision of temporary berth	247 days	Mon 04/11/15	Tue 05/7/19	
125	Design and ICE checking of temporary berth	80 days	Mon 04/11/15	Wed 05/2/2	
126	Submission for Engineer's comment	81 days	Thu 05/2/3	Sun 05/4/24	125
127	Piling (Phase 1)	31 days	Mon 05/4/25	Wed 05/5/25	123,126,117,25,30,25,42
128	Piling (Phase 2)	9 days	Fri 05/6/10	Sat 05/6/18	56
129	Deck construction and installation of fenders	25 days	Sun 05/6/19	Wed 05/7/13	128
130	Relocation of navigation light by Marine Dept.	81 days	Mon 05/4/25	Thu 05/7/14	
131	Application to Marine Department	80 days	Mon 05/4/25	Wed 05/7/13	
132	Relocation works	1 day	Thu 05/7/14	Thu 05/7/14	130,131
133	Certified by ICE, testing and commissioning of berth	5 days	Fri 05/7/15	Tue 05/7/19	132
134	Demolition of part of the existing pier	115 days	Mon 05/4/18	Wed 05/8/10	
135	Survey of existing structures	31 days	Mon 05/4/18	Wed 05/5/18	
136	Design and ICE checking of demolition plan	32 days	Thu 05/5/19	Sun 05/6/19	115

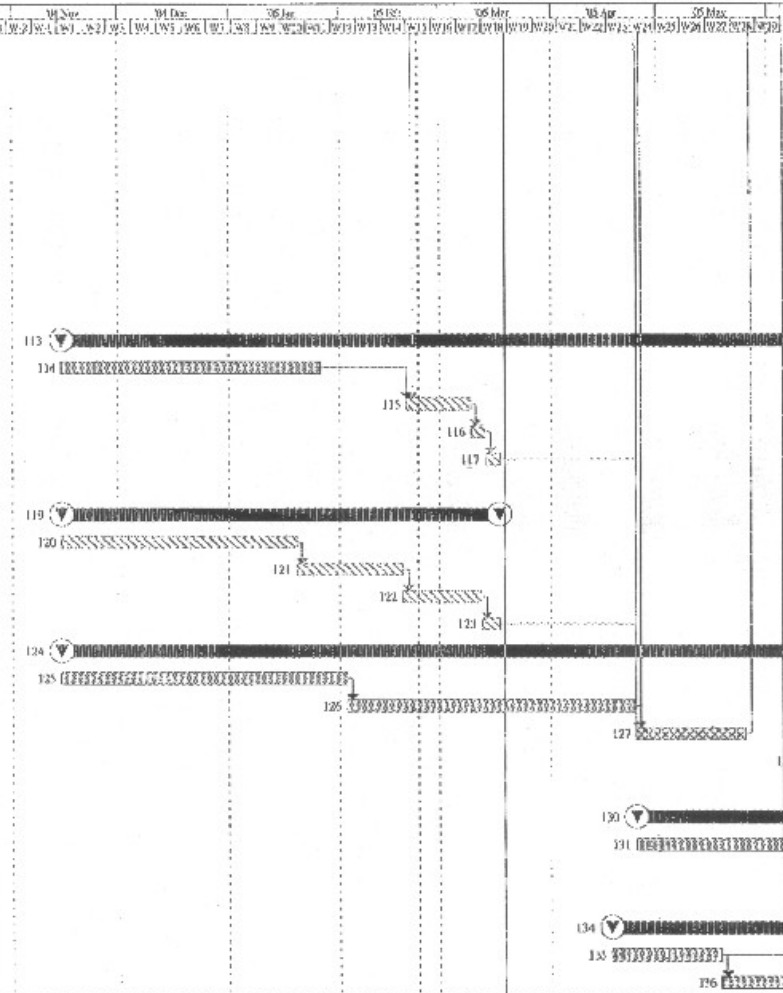

CV/2004/02/0204/02 Master Programme (Version 1.1)

Normal Task	000000000000	Pages	██████████	Summary	██████████	Critical Task (Sec. 1 & 2)	000000000000	Critical Task (Sec. 2)	000000000000
Split	.....	Commencement Milestone	██████████	Completion Milestone	██████████	Critical Task (Sec. 1)	000000000000	Maintenance Period	000000000000

Page 4

#2563 P.025 /013

#2563 P.025 /013




Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

### Master Programme (Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

Task No.	Task Name	Duration	Start	Finish	Resources
137	Submission for Engineer's comments	30 days	Mon 05/6/20	Tue 05/7/19	336
138	Consult with local residents	30 days	Mon 05/6/20	Tue 05/7/19	337
139	Demolition	22 days	Wed 05/7/20	Wed 05/8/10	193,138,197
140	Ground investigation	129 days	Wed 04/12/29	Fri 05/5/6	
141	Submission for Engineer's comment	69 days	Wed 04/12/29	Sun 05/3/26	
142	Ground investigation works on site	20 days	Fri 05/3/18	Wed 05/4/6	141,201,17
143	Preparation and approval of reports	10 days	Thu 05/4/7	Sat 05/4/16	142
144	Submission of reports to determine pile founding levels	20 days	Sun 05/4/17	Fri 05/5/6	143
145	Piling for permanent pier	342 days	Sat 05/1/1	Thu 05/12/8	
146	Compilation of method statement for piling	33 days	Sat 05/1/1	Wed 05/2/2	
147	Submission for Engineer's comment	189 days	Thu 05/2/3	Wed 05/8/10	146
148	Vertical preliminary pile and testing	15 days	Thu 05/8/11	Thu 05/8/25	147,139,45,144
149	Vertical main piles (E1,E4,D1,D4,C1,C4)	20 days	Fri 05/8/26	Wed 05/9/14	148
150	Temporary platform for raking pile	21 days	Thu 05/9/15	Wed 05/10/5	149
151	Vertical main pile (remaining 15 nos)	45 days	Thu 05/9/15	Sat 05/10/29	148
152	Raking preliminary piles and testing	16 days	Thu 05/10/6	Fri 05/10/21	150,62
153	Raking main piles (remaining 9 nos)	33 days	Sat 05/10/22	Wed 05/11/23	152
154	Pile tests for main piles	15 days	Thu 05/11/24	Thu 05/12/8	151,153
155	Construction of pile cap and deck	201 days	Wed 05/8/10	Sun 06/2/26	
156	Submission and approval of precast yard	60 days	Wed 05/8/10	Sat 05/10/8	
157	Casting of precast units at precast yard	60 days	Mon 05/10/10	Thu 05/12/8	156
158	Design and ICE checking of falsework for pile cap and deck construction	60 days	Sat 05/9/10	Tue 05/11/6	
159	Submission of calculation and method statement for Engineer's approval	30 days	Wed 05/11/9	Thu 05/12/8	158
160	Erection of falsework for installation of precast units	20 days	Fri 05/12/9	Wed 05/12/28	159,154
161	Installation of precast units with in-situ pile caps	55 days	Fri 05/12/9	Wed 06/2/1	159,154
162	Casting of in-situ pier deck	25 days	Thu 06/2/2	Sun 06/2/26	161,161
163	Construction of bollards	25 days	Thu 06/2/2	Sun 06/2/26	161
164	Installation of corrosion monitoring system	85 days	Sun 05/12/4	Sun 06/2/26	
165	Approval of specialist contractor and method statement	60 days	Sun 05/12/4	Wed 06/2/1	
166	Installation of corrosion monitoring system	25 days	Thu 06/2/2	Sun 06/2/26	161,165
167	Construction of villa	110 days	Fri 06/2/17	Tue 06/6/6	
168	Concrete structure	50 days	Mon 06/2/27	Mon 06/4/17	162
169	Finswing	110 days	Fri 06/2/17	Tue 06/6/6	
170	Material submission	60 days	Fri 06/2/17	Mon 06/4/17	
171	Construction	50 days	Thu 06/4/18	Tue 06/6/6	168,170

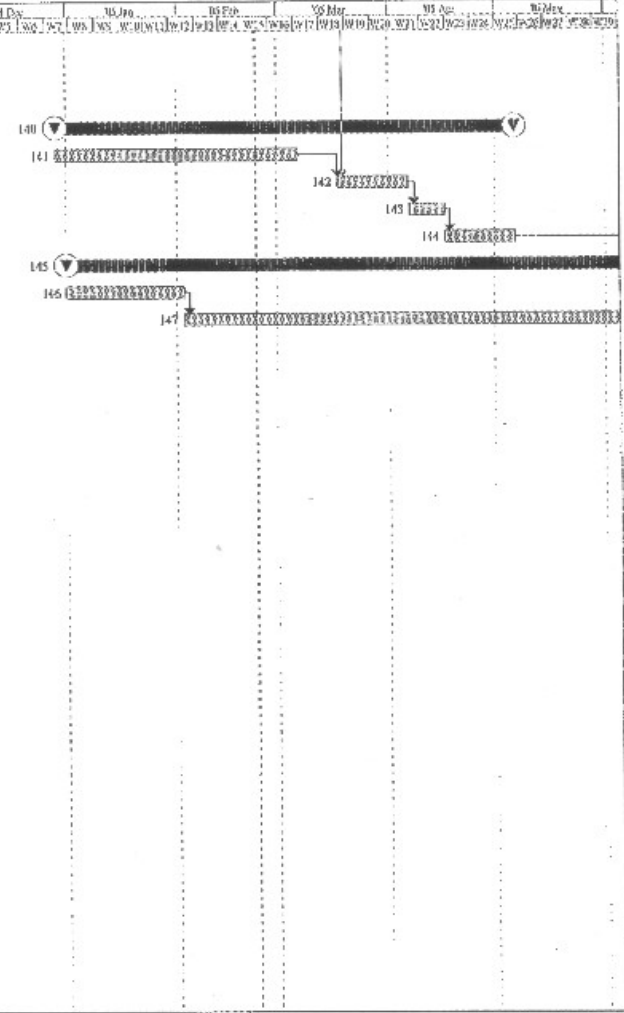

Contract No.: CV/2004/02  
 Version: 2  
 Name: Task  
 Split:   
 Progress:   
 Summary:   
 Commencement Milestone:   
 Completion Milestone:   
 Critical Task (Sec 1 & 2):   
 Critical Task (Sec 1):   
 Critical Task (Sec 2):   
 Maintenance Period:   
 Page 5

PRB. 23.2005.17:02

#2663 P.006 /013

### Master Programme (Version 2)

SI	Task Name	Duration	Start	Finish	Predecessors	Calendar												
						01 Nov	01 Dec	01 Jan	01 Feb	01 Mar	01 Apr	01 May	01 Jun	01 Jul	01 Aug	01 Sep	01 Oct	01 Nov
27	Construction of walking cover 1 & 2	245 days	Wed 05/10/05	Tue 06/06/06														
27	Approval of specialist contractor	60 days	Wed 05/10/05	Sat 05/12/05														
27	Submission of workshop drawings for connection details with deck	60 days	Sun 05/12/04	Wed 06/2/1	177													
27	Material submissions	85 days	Sun 05/12/04	Sun 06/2/26	177													
27	Submission of workshop drawing for remaining roof system	85 days	Sun 05/12/04	Sun 06/2/26	177													
27	Construction of steel works	50 days	Mon 06/2/27	Mon 06/4/17	177, 182, 195													
27	Erection of roof covers	50 days	Tue 06/4/18	Tue 06/6/06	177													
27	Electrical system, CLP meter box and lighting system	200 days	Tue 05/11/29	Fri 06/6/16														
27	Approval of specialist contractor	30 days	Tue 05/11/29	Wed 05/12/28														
27	Liaison with CLP and EMSD	60 days	Thu 05/12/29	Sun 06/2/26	180													
27	Installation	100 days	Mon 06/2/27	Tue 06/6/06	181, 182													
27	Testing	10 days	Wed 06/6/07	Fri 06/6/16	182													
27	Construction of floor finish	130 days	Thu 06/3/9	Sun 06/7/16														
27	Material submission	90 days	Thu 06/3/9	Tue 06/6/06														
27	Site works	40 days	Wed 06/6/07	Sun 06/7/16	177, 185, 191													
27	Construction of hand railing, seating benches and notice boards	150 days	Fri 06/2/17	Sun 06/7/16														
27	Material submission	60 days	Fri 06/2/17	Mon 06/4/17														
27	Construction	90 days	Tue 06/4/18	Sun 06/7/16	183													
27	Installation of fender system	190 days	Sun 06/1/8	Sun 06/7/16														
27	Material submission	31 days	Sun 06/1/8	Tue 06/2/9														
27	Ordering of material	59 days	Wed 06/2/8	Fri 06/4/7	191													
27	Site works	100 days	Sat 06/4/8	Sun 06/7/16	192													
27	Relocation of navigation light by Marine Dept.	92 days	Mon 06/4/17	Mon 06/7/17														
27	Application to Marine Department	91 days	Mon 06/4/17	Sun 06/7/16														
27	Relocation	1 day	Mon 06/7/17	Mon 06/7/17	183, 193, 195, 196, 199													
27	Commissioning of the pier	1 day	Tue 06/7/18	Tue 06/7/18	186													
27	Demolition of the temporary berth and the existing pier	141 days	Sun 06/3/19	Sun 06/8/6														
27	Survey to existing structure	31 days	Sun 06/3/19	Tue 06/4/18														
27	Design and ICE checking of demolition plan	61 days	Wed 06/4/19	Sun 06/6/18	186													
27	Submission for Engineer's comments	30 days	Mon 06/6/19	Tue 06/7/18	200													
27	Liaison with local residents	30 days	Mon 06/6/19	Tue 06/7/18	200													
27	Demolition	19 days	Wed 06/7/19	Sun 06/8/6	183, 184, 200													
27	Maintenance Period for the Works	365 days	Mon 06/8/7	Mon 07/8/6	203													

Contract No.: CV/2004/02 Master Programme (Version 2)	<b>Network Task</b>		<b>Progress</b>		<b>Summary</b>		<b>Critical Task (Sec 1 &amp; 2)</b>		<b>Critical Task (Sec 2)</b>	
	<b>Split</b>		<b>Commencement Month</b>		<b>Completion Month</b>		<b>Critical Task (Sec 1)</b>		<b>Maintenance Period</b>	


Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme

(Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

FEB. 23. 2005 17:03

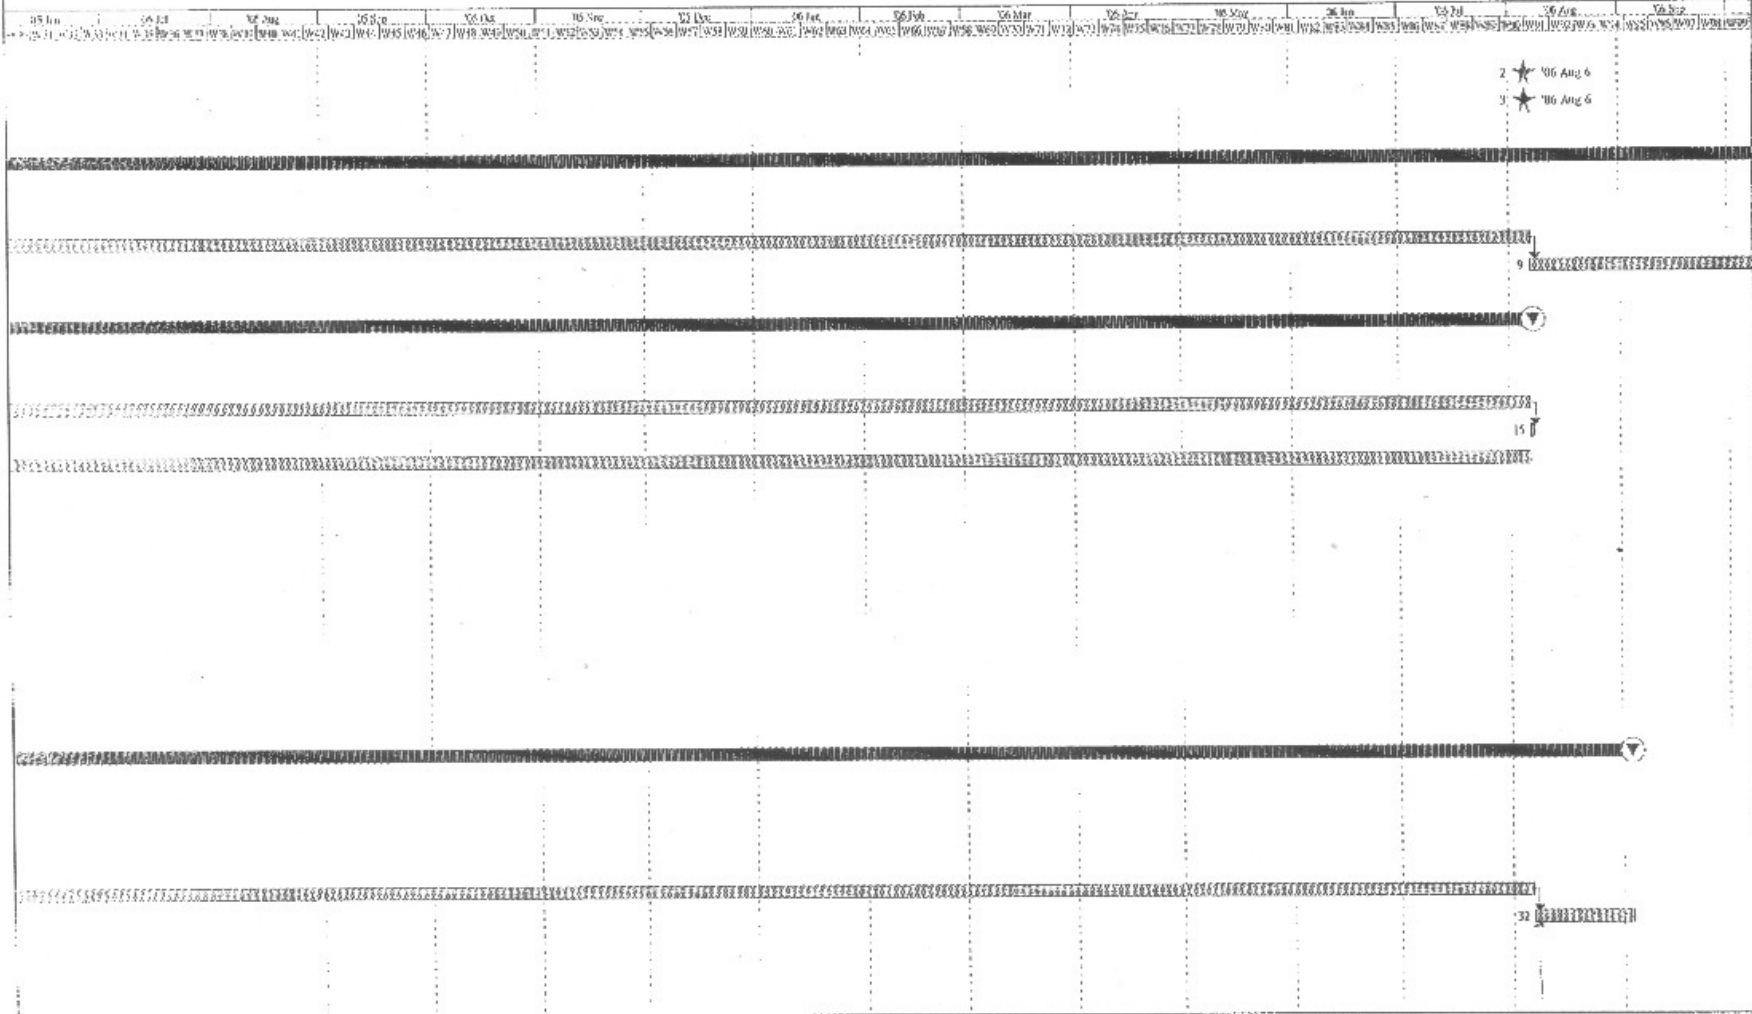

#2663 P. 008 / 013

Contract No.: CV/2004/02 Master Programme (Version 2)	Normal Task: ██████████ Split: .....	Progress: ██████████ Commencement Milestone: ○	Summary: ██████████ Completion Milestone: ●	Critical Task (Sec 1 & 2): ██████████ Critical Task (Sec 1): ██████████	Critical Task (Sec 3): ██████████ Maintenance Period: ██████████	Other Task: ██████████
--	---	---	--	--	---	------------------------


Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme

(Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

FEB 23 2005 17:04

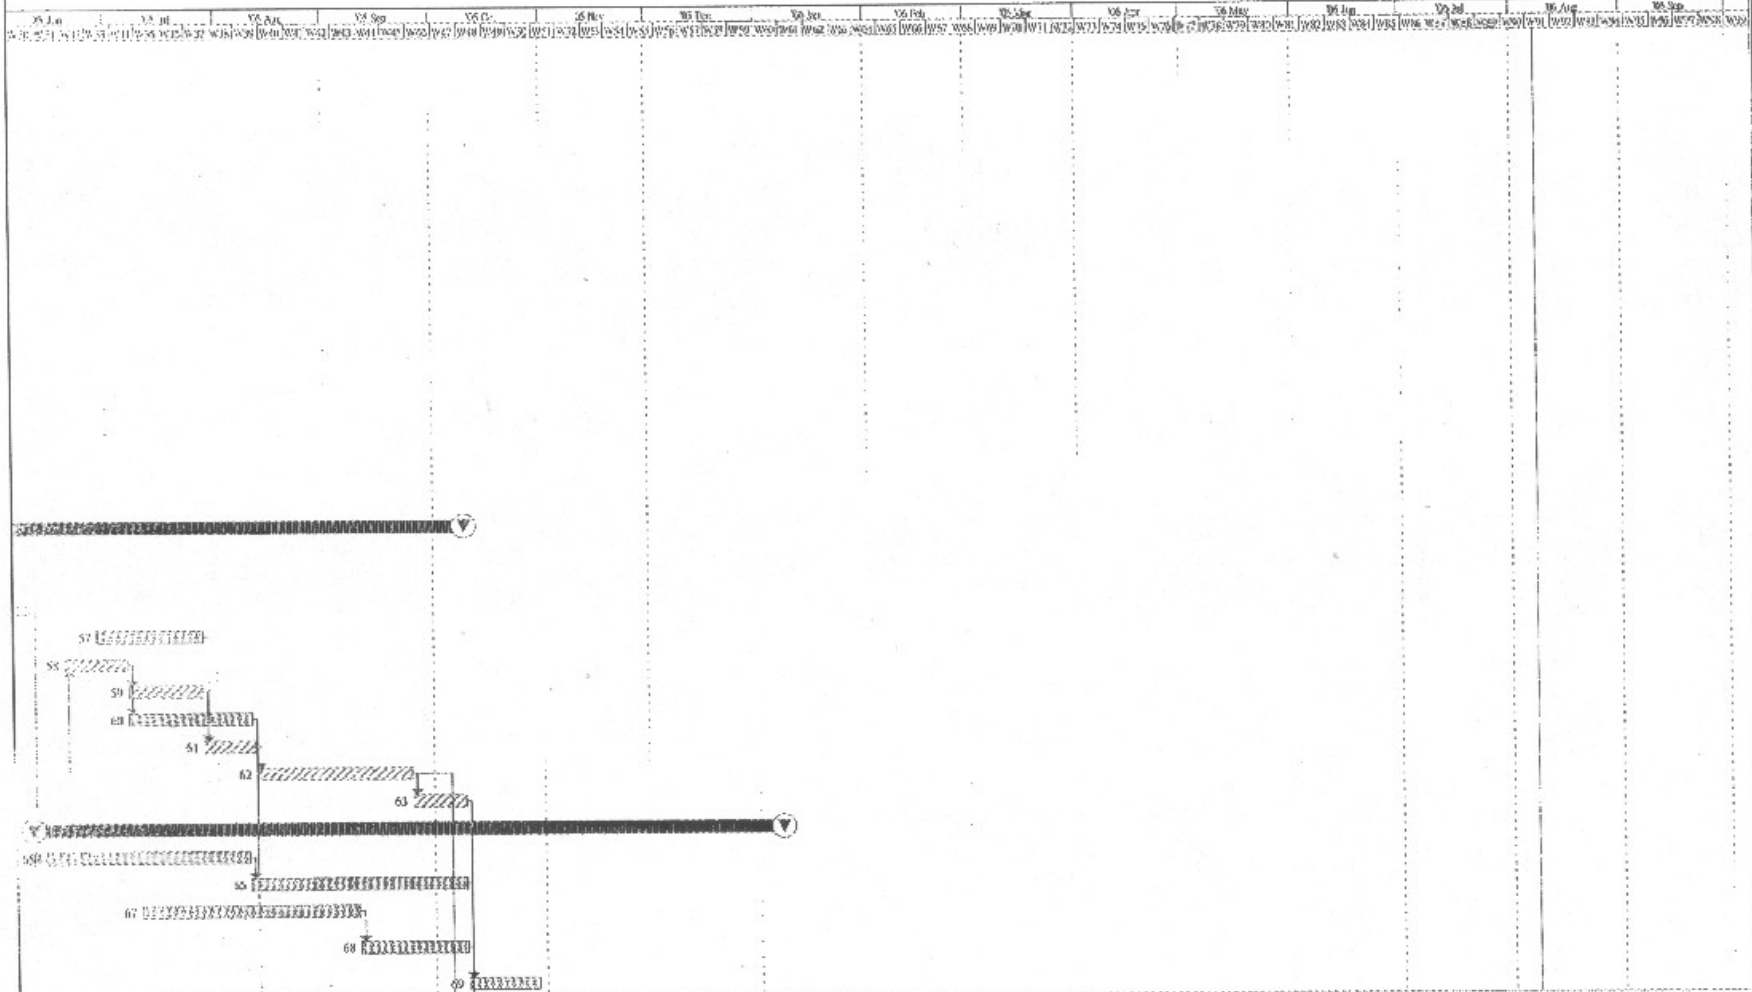

#2663 P.009 /013

Contract No.: CV/2004/02 Master Programme (Version 2)	Name of Task: 82/3	Progress: .....	Summary: Completion Milestone	Critical Task (Sec 1 & 2)	Critical Task (Sec 1)	Critical Task (Sec 2) Maintenance Period
--	--------------------	-----------------	-------------------------------	---------------------------	-----------------------	---


Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme

(Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

FEB 23, 2005 1:7:04

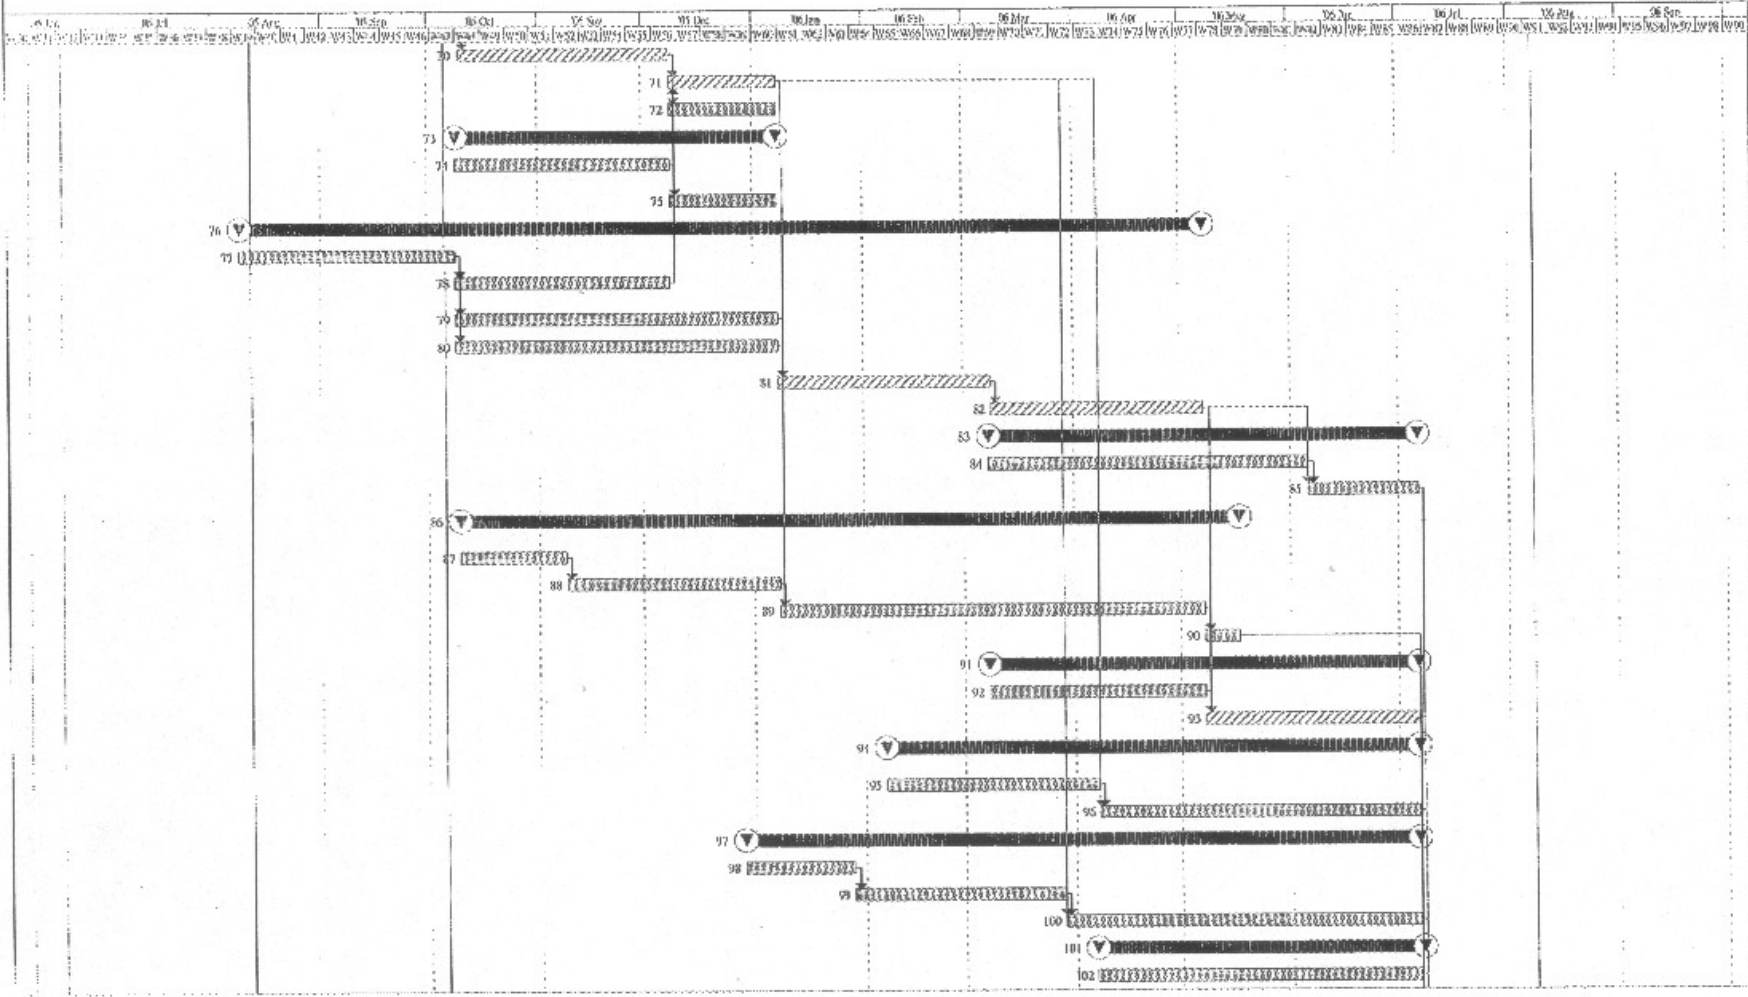


Contract No.: CV/2004/02 Master Programme (Version 2)	Normal Task		Freeze		Summary		Critical Task (Sec: 1 & 2)		Critical Task (Sec: 2)	
	Split		Commencement Milestone		Completion Milestone		Critical Task (Sec: 1)		Maintenance Period	

#2663 P.010 /013

Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme (Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005

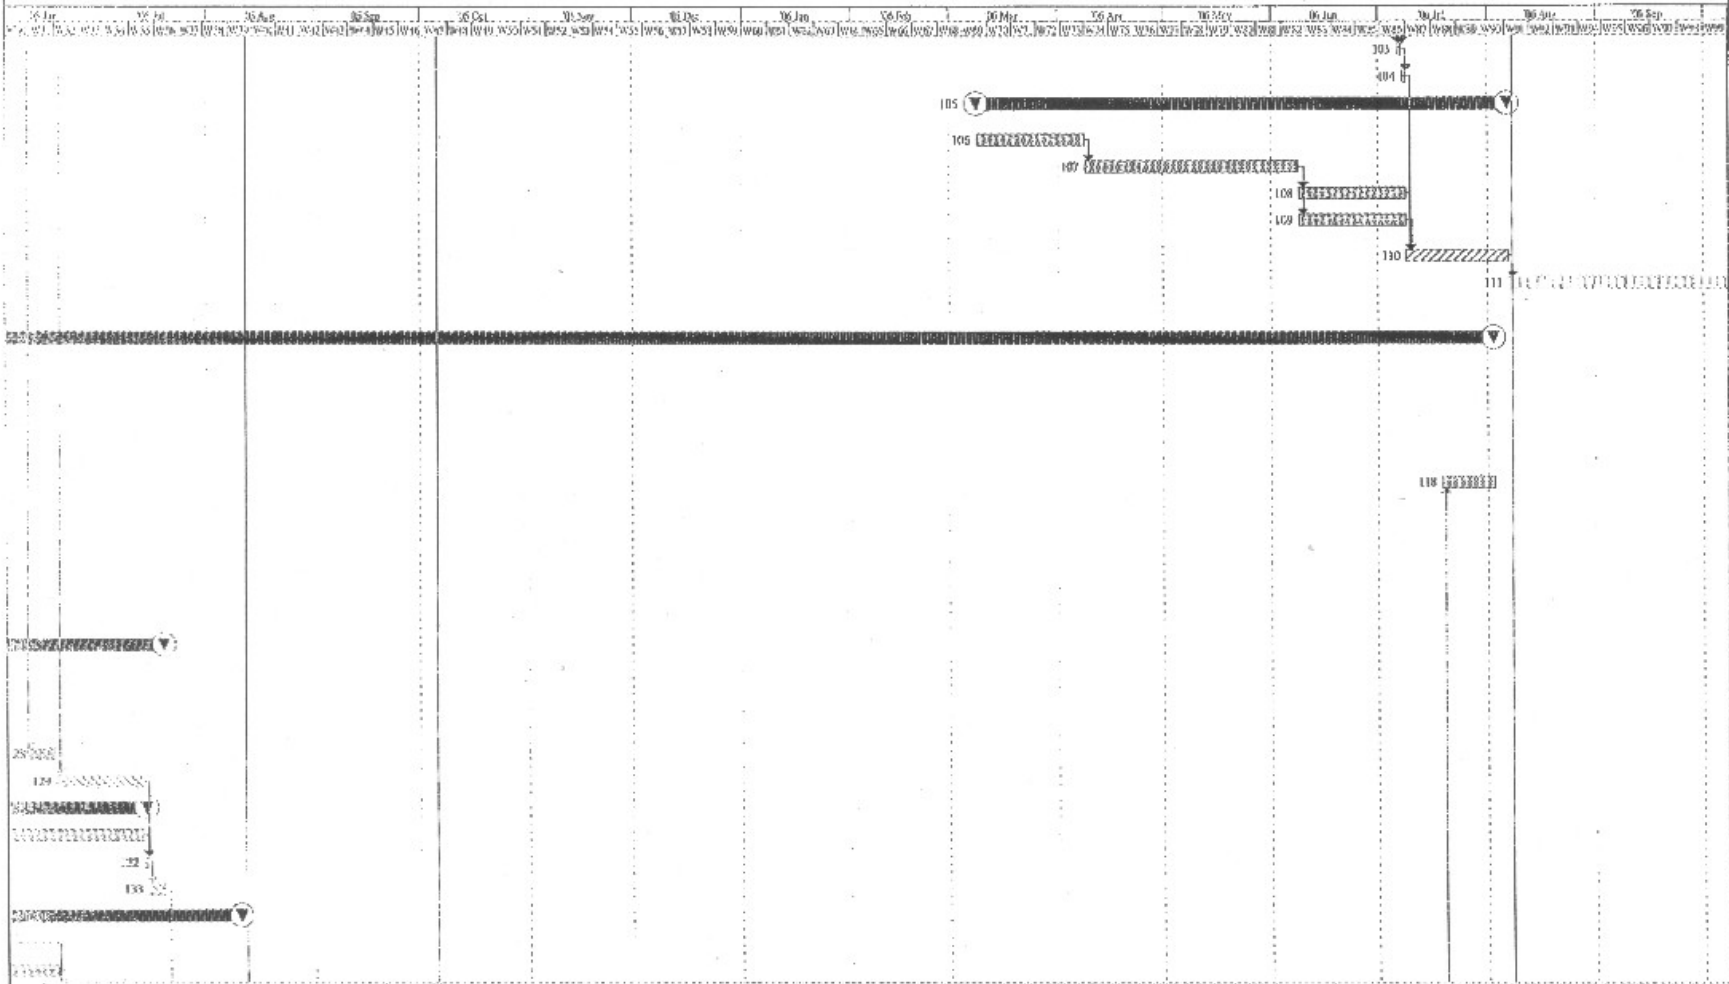

Contract No.: CV/2004/02  
 Master Programme (Version 2)

Normal Task	██████████	Progress	██████████	Summary	○	Control Task (Sec 1 & 2)	██████████	Critical Task (Sec 2)	██████████
SPL	.....	Commencement Milestone	○	Completion Milestone	○	Control Task (Sec 3)	██████████	Maintenance Period	██████████

ZBB.23.2005.17:05

#2663 P.011 /013


Contract No.: CV/2004/02  
 Reconstruction of Wong Shek and  
 Ko Lau Wan Public Piers

# Master Programme

(Version 2)

Contractor: Kin Shing Construction Co. Ltd.  
 Commencement Date: 15th Nov 2004  
 Completion Date: 6th Aug 2006  
 Programme Date: 21st Feb 2005


#2663 P.012 /013

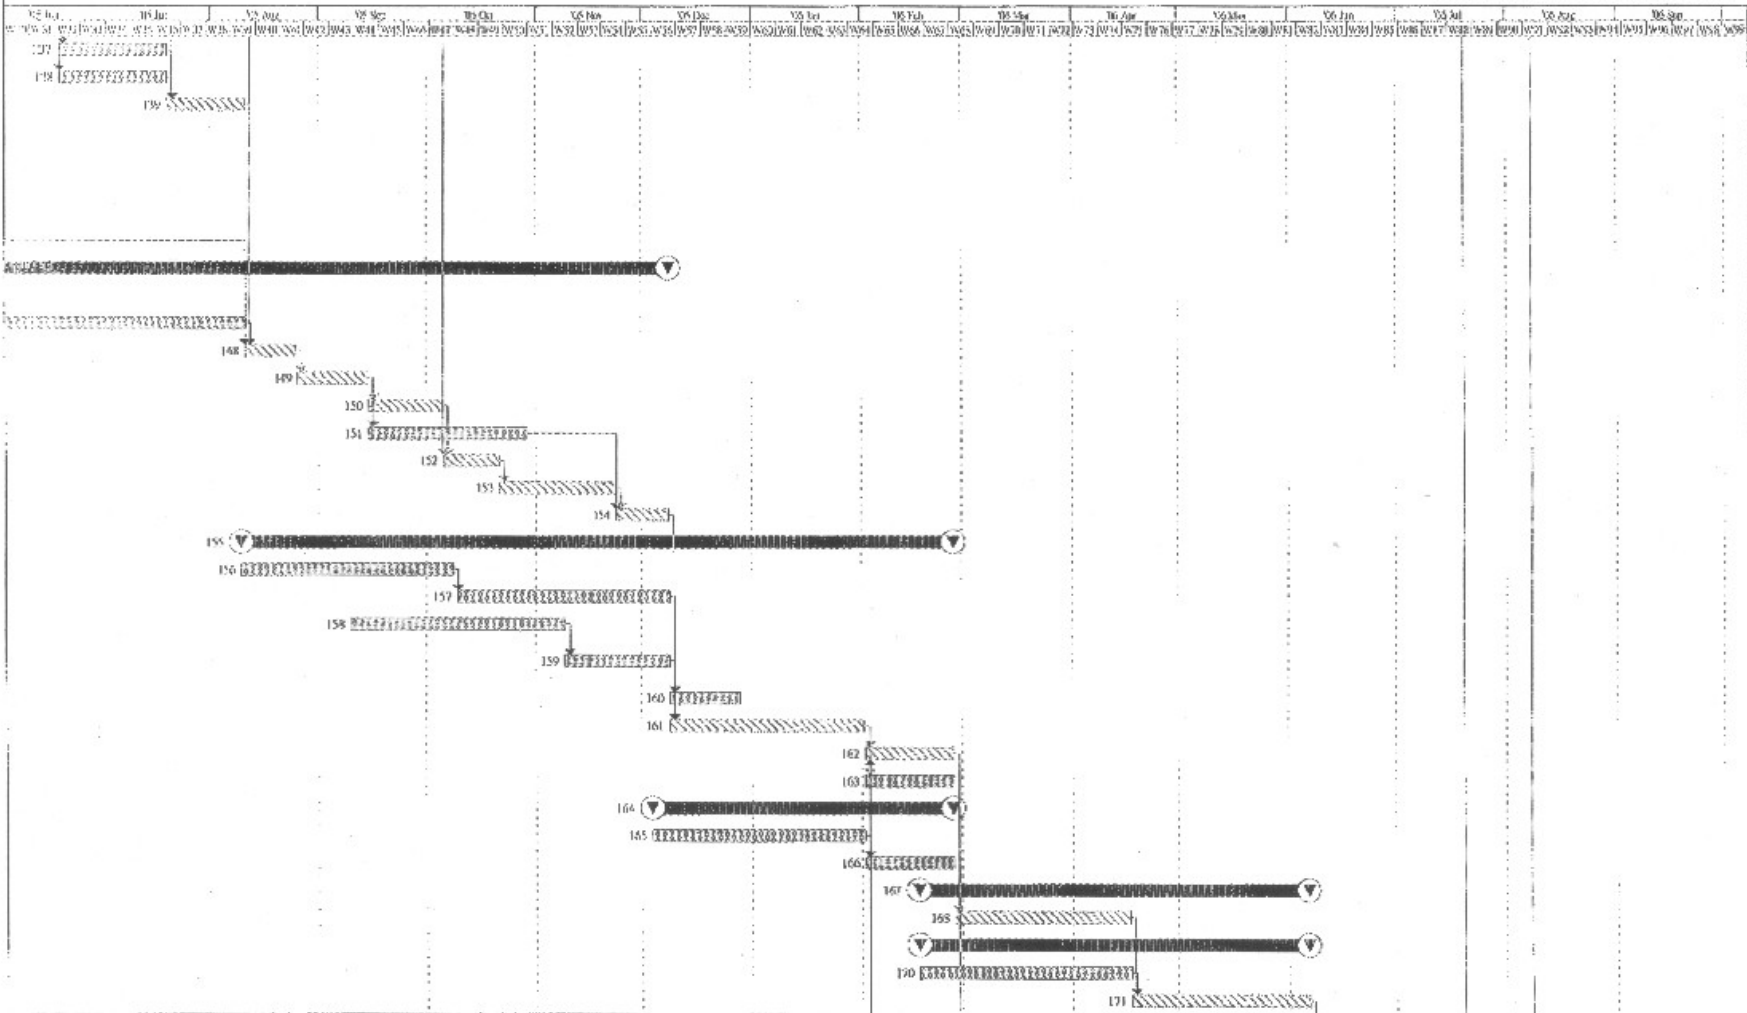

Contract No.: CV/2004/02 Master Programme Version 21	Master Task 139-171	Progress	Summary	Critical Task (Sec 1 & 2)	Critical Task (Sec 2)
Start	Commencement Milestone	Completion Milestone	Critical Task (Sec 1)	Maintenance Period	

#2663 P.012 /013

# Master Programme (Version 2)

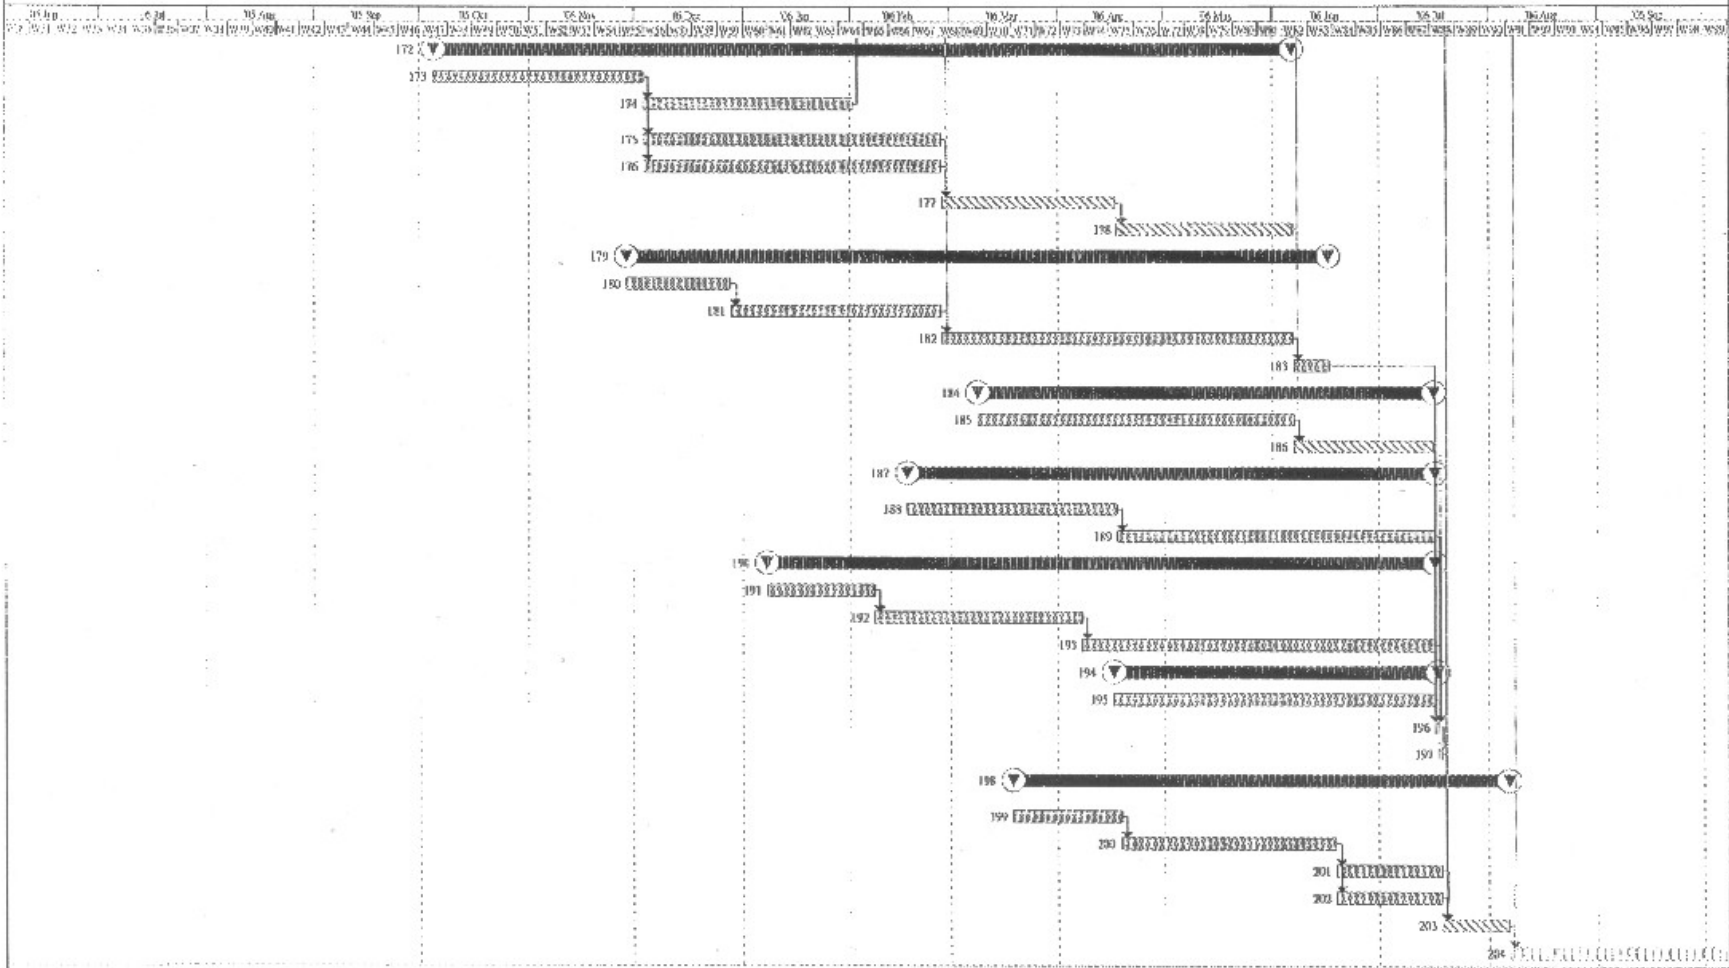

Contract No.: CV/2004/02  
 Master Programme (Version 2)

Normal Task		Progress		Security		Critical Task (Sec 1 & 2)		Critical Task (Sec 2)	
Split		Commencement Milestone		Completion Milestone		Critical Task (Sec 1)		Milestone Point	

#2663 P.013 / 013

#2663 P.013 / 013
