EP-01/097/2001/C

Provision of EM&A Services at Water Recreation Centre

Monthly EM&A Report No.64 (16 November to 15 December 2010)

December 2010

	Name	Signature
Prepared & Checked:	Y W Fung	V
Reviewed & Approved:	Y T Tang	Captaling

Version:	0	Date:	30 December 2010

Disclaimer

This report is prepared for Hong Kong International Theme Parks Limited and is given for its sole benefit in relation to and pursuant to EP-01/097/2001/C and may not be disclosed to, quoted to or relied upon by any person other than Hong Kong International Theme Parks Limited without our prior written consent. No person (other than Hong Kong International Theme Parks Limited) into whose possession a copy of this report comes may rely on this report without our express written consent and Hong Kong International Theme Parks Limited may not rely on it for any purpose other than as described above.

AECOM Asia Co. Ltd.

11/F, Grand Central Plaza, Tower 2, 138 Shatin Rural Committee Road, Shatin, NT, Hong Kong Tel: (852) 3105 8686 Fax: (852) 2317 7609 www.aecom.com

Water Recreation Centre (Monthly EM&A Report No. 64)

Submitted by AECOM Asia Co. Ltd. on 16 December 2010

This is to verify that:

The Water Recreation Centre Monthly EM&A Report No. 64

Submitted by: AECOM Asia Co. Ltd.

On: 16 December 2010

Has been verified by the undersigned.

Signed

Ir Dr Anne Watker-Zeris

Independent Environmental Checker (IECK)

Retained by Hongkong International Theme Parks Ltd

pursuant to EP No. EP-01/97/2001/C

Date

17 December 2010

TABLE OF CONTENTS

*			Page
EXE	CUTIVE SUMI	MARY	1
	Implementa Environmei	ntal Monitoring Works ation Status of Environmental Mitigation Measures ntal Complaints and Prosecution	l l
1.	INTRODUC	CTION	1
	Project Org	d janisation of the EM&A Requirements	1
2.	ENVIRON	MENTAL AUDIT	2
		ation Status of Environmental Mitigation Measures	
		nvironmental Licensing and Permitting	
		agement ation Status of Environmental Complaint Handling Procedures	
3.	•	IONS AND RECOMMENDATIONS	4
.		s	
		sdations	
List	of Tables	O Control of the Cont	0
	Table 2.1	Summary of Environmental Notification, Licensing and Permit Status	Z
List	of Figures		
	Figure 1.1 Figure 1.2	Location of Water Recreation Centre Project Organization	
List	of Appendices	s	
	Appendix A Appendix B Appendix C	Contact of Key Environmental Personnel Summary of Environmental Mitigation Implementation Schedule Complaint Flow Diagram and Complaint Log	

EXECUTIVE SUMMARY

This is the sixty-fourth monthly Environmental Monitoring and Audit (EM&A) report prepared by AECOM Asia Co. Ltd. (integrating the operation of ENSR Asia (HK) Ltd.), the designated Environmental Team (ET), for the project "Provision of EM&A Services at Water Recreation Centre". The Water Recreation Centre (WRC) commenced operation on 16 August 2005.

This report presents the results of environmental audit works conducted between 16 November 2010 and 15 December 2010.

Environmental Monitoring Works

Environmental Licensing and Permitting

Environmental permit (No. EP-01/097/2001/C) was issued to the Hongkong International Theme Parks Limited (HKITP) for the operation of WRC. HKITP has been registered as chemical waste producer (Waste Producer No. 9499-973-H3095-01).

Implementation Status of Environmental Mitigation Measures

Monthly environmental site inspection was carried out on 13 December 2010. Environmental mitigation measures as recommended in the EIA report, Operational EM&A Plan and EP-01/097/2001/C were properly implemented.

Environmental Complaints and Prosecution

No complaint, summons or prosecution related to environmental issues was made against the Project in the reporting period.

Future Key Issues

The operator of WRC is reminded to continue to implement measures as recommended in the EIA Report, Operational EM&A Plan and EP-01/097/2001/C.

Į

Revision 0

1. INTRODUCTION

Background

- 1.1 AECOM Asia Co. Ltd. (integrating the operation of ENSR Asia (HK) Ltd.) (hereinafter referred as the "ET") was appointed by Hongkong International Theme Park Ltd. (HKITP) (hereinafter referred as the "Operator") to carry out operational Environmental Monitoring and Audit at the Water Recreation Centre since its operation on 16 August 2005. Under the requirements of Section 4 of the Environmental Permit EP-01/097/2001/C, EM&A programme is required to be implemented in accordance with the Operational EM&A Plan approved by the Environmental Protection Department (EPD) on 31 August 2005.
- 1.2 The WRC is a portion of the Contract for "Theme Park and Associated Infrastructures at Penny's Bay", which encompasses an area of approximately 12 ha and contains a multi-function artificial lake, water-based and land-based recreational facilities and ancillary facilities. Apart from recreation purpose, the lake water is a source of irrigation water for the entire Penny's Bay. The location of the WRC is given in Figure 1.1.
- 1.3 Following approval of the EIA, an Environmental Permit (EP) was issued to the Civil Engineering Department (CED) (now Civil and Engineering Development Department (CEDD) and the subsequent variation of the permit no. EP-097/2001/B and EP-138/2002/C contain the requirements and obligations on the Environmental Monitoring and Audit (EM&A) during the operation of the WRC. Under the Contract for "Theme Park and Associated Infrastructures at Penny's Bay", the WRC and ancillary facilities were designed and constructed under the supervision of CEDD and the WRC would be turned over from CEDD to HKITP for operation upon completion of construction. Environmental permit no. EP-01/097/2001/C was issued to the HKITP for the operation of WRC.
- 1.4 This report presents the results of environmental audit works conducted between 16 November 2010 and 15 December 2010.

Project Organisation

1.5 The structure of the environmental management team is shown in Figure 1.2. Contacts of key environmental staff of the Project are shown in Appendix A.

Summary of the EM&A Requirements

- 1.6 The latest EM&A programme requires environmental audit at the WRC. The purpose of the audit was to ensure all environmental mitigation measures, as recommended in the EIA report, Operational EM&A Plan and EP-01/097/2001/C, were properly implemented.
- 1.7 Site audit and the status of environmental licensing and permits are described in Section 2.
- 1.8 Summary of the advice on the implementation status of environmental protection and pollution control/mitigation measures is summarised in Section 2 of the Report.

Revision 0 1

2. ENVIRONMENTAL AUDIT

Implementation Status of Environmental Mitigation Measures

- 2.1 Site audit was carried out on a monthly basis to monitor environmental issues to ensure that all mitigation measures were implemented timely and properly.
- 2.2 Monthly site inspection was carried out on 13 December 2010. Environmental mitigation measures for water quality, waste management, landscape and visual, as recommended in the EIA report, Operational EM&A Plan and EP were properly implemented. There was no specific observation requiring following up action. In general, the condition of the WRC was satisfactory:
 - No floating refuse was observed.
 - No uncontrolled surface runoff into the lake was observed.
 - No algicide was applied to the WRC.
 - No discharge was made from the WRC into marine water.
 - No improper storage of oil/chemicals was observed.
 - Environmental Permit was kept in the site office and was available for inspection upon request.
- 2.3 A summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in Appendix B.

Status of Environmental Licensing and Permitting

2.4 All permits/licences/notifications obtained as of the reporting period are summarised in Table 2.1

Table 2.1 Summary of Environmental Notification, Licensing and Permit Status

Di4 N-	Valid Period		Description	Status	
Permit No. From To		То	Description		
Environmental Perm	nit				
EP-01/097/2001/C	19 Oct. 05	-	Operation of an approximately 32 ha water recreation centre with a 12 ha multi-function artificial lake, water-based and land-based recreational facilities and ancillary facilities		
Chemical Waste Reg	gistration				
9499-973-H3095-01	29 Jul. 05	-	Theme Park at Penny's Bay Vali		

Waste Management

- 2.5 Waste management of WRC was implemented as stipulated in the Waste Management Plan.
- 2.6 As waste management of WRC was undertaken as part of the overall Theme Park Resort waste management scheme, records of waste handling and disposal would be reported in the Theme Park EM&A Report.

Revision 0 2

Implementation Status of Environmental Complaint Handling Procedures

- 2.7 Appendix C presents the environmental complaint flow diagram of the Project.
- 2.8 No complaint, summons or prosecution related to environmental issues was received or made against the Project in the reporting period.

Revision 0 3

3. CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 3.1 Environmental audit was carried out on 13 December 2010 in accordance with the Operation EM&A Plan. No non-compliance was observed during the inspection. In general, the condition of the WRC was satisfactory.
- 3.2 Environmental mitigation measures as recommended in the EIA Report, Operational EM&A Plan and EP were properly implemented.
- 3.3 No complaint, summons or prosecution related to environmental issues was made against the Project in the reporting period.


Recommendations


3.4 The operator of WRC is reminded to continue to implement measures as recommended in EIA Report and EP.

4

Revision 0

GI	ID	ᄄᅂ

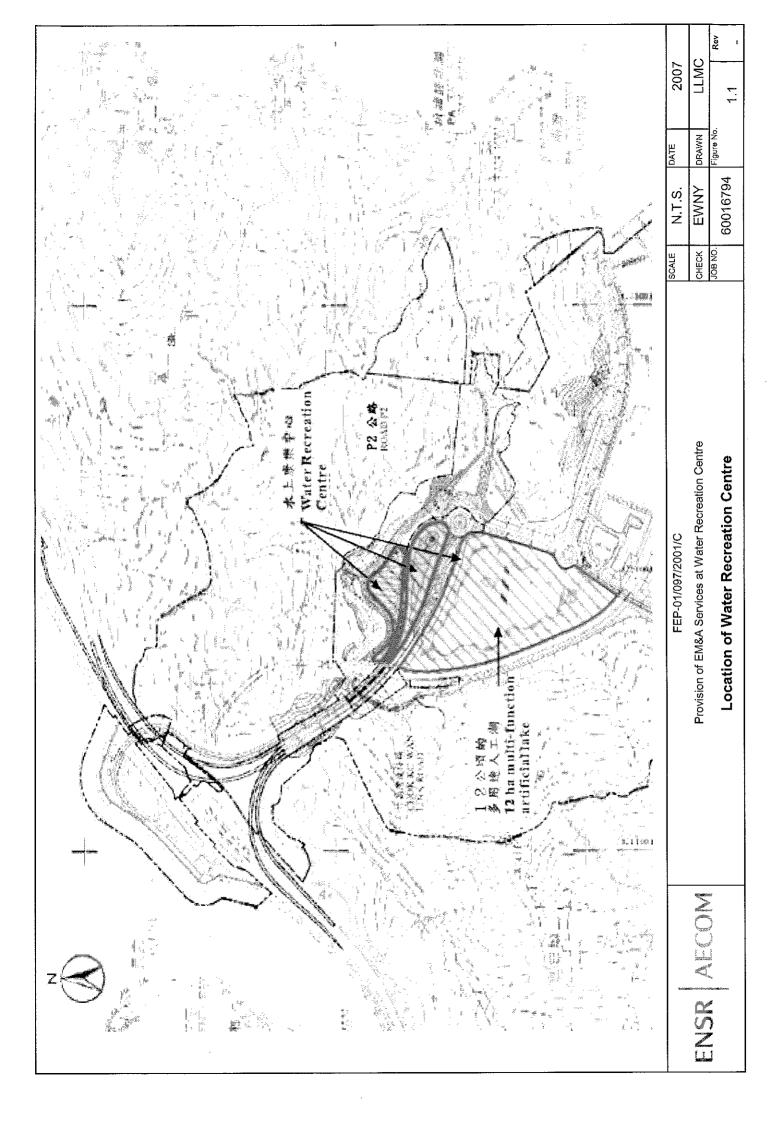

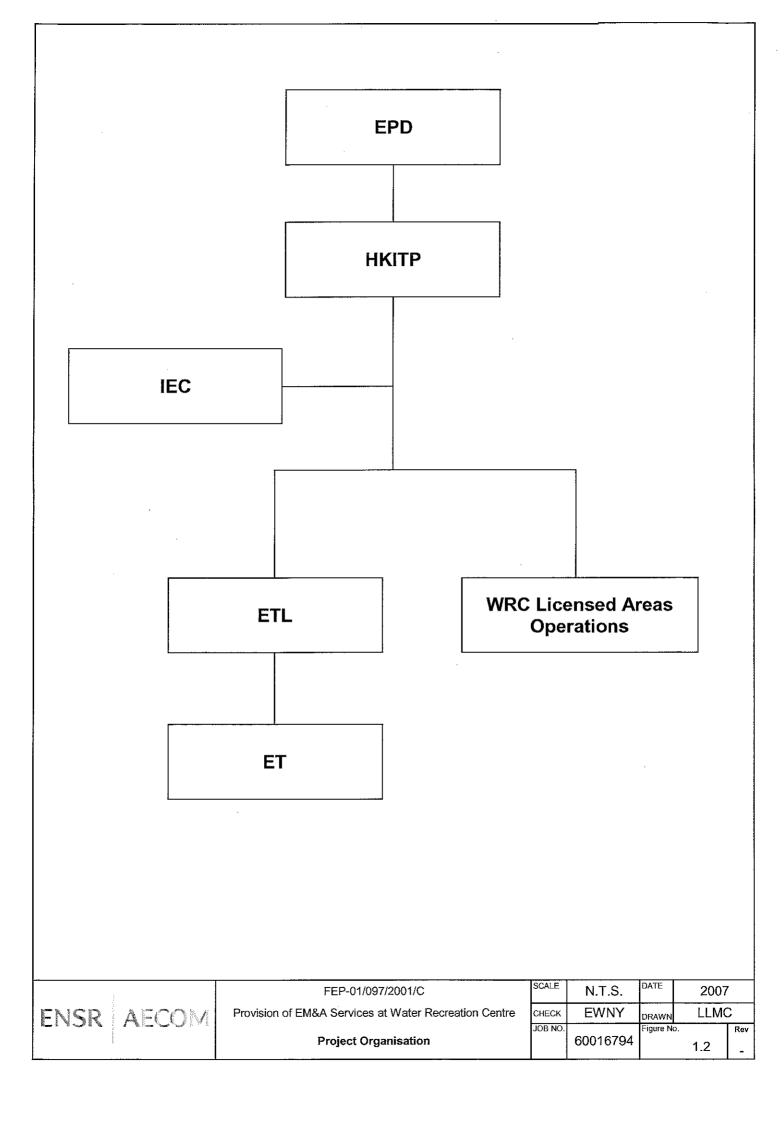

APPENDIX A CONTACTS OF KEY ENVIRONMENTAL PERSONNEL

Appendix A: Contacts of Key Environmental Staff

	<u>Name</u>	<u>Telephone</u>	<u>Fax</u>
IEC Mott MacDonald Independent Environmental Checker	Dr. Anne Watker-Zeris	2828 5757	2827 1823
ET AECOM Asia Co. Ltd. Environmental Team Leader Environmental Scientist	Mr. Y T Tang Mr. Y W Fung	2893 1551 2893 1551	2891 0305 2891 0305

APPENDIX B SUMMARY OF ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

Appendix B — Summary of Environmental Mitigation Implementation Schedule

Reference	Mitigation Measures		Status
	Water Quality		
EIA Report 5 11 2	The lake shall be lined with an impermeable liner. However, as such liners may have a limited life span, beyond which the particular and detailed the lines that lines the lines that the manifest may have a limited life span is reached.	the the	7
2.1.1.5	periormance may deteriorates, the mist shall be replaced once the manufacturer substantial teached.		
EIA Heport	• Stormwater run-off from surrounding hillsides shall pass through silt traps prior to entering the artificial lake to prevent		
ν. 	sination. The silt traps strait be designed to flave adequate capacity to retain any sinvectinities contained within the stormwater. The silt traps shall be frequently maintained/cleaned to prevent a deterioration in performance.		>
EIA Report	Should the quality of the water in the Tai Lam Chung Reservoir deteriorate below the present levels an alternate supply of	oly of	
5.11.2, EP	water, of a quality at least as good as that within the Tai Lam Chung Reservoir, shall be used to 'top up' the water within the	hin the	N/A
3.7	lake.		
EIA Report	If it becomes necessary to add an algicide to the lake to control algal growth, the algicide shall be biodegradable with a short	a short	
5,11.2, EP	half life of three days or less. During use of the algicide discharge of the lake water to the marine waters shall be prohibited,	hibited,	- V
3.8, 3.9	until the algicide has decayed. The algicide shall not be used during periods of heavy rainfall when overflow of the lake is	(e is	<u> </u>
	possible.		
EIA Report	Stormwater from any urban/developed areas shall not be allowed to enter the lake as they may contain pollutants. Sewage	ewage	
5.11.2, EP	effluent from the water recreation centre shall be transported to the sewerage mains for conveyance to the Siu Ho Wan STW	an STW.	~
3.6			
EIA Report	 Any fuel for motorised water sports vessels shall be stored in bunded areas, of at least 110% capacity of the largest fuel 	nel	
5.11.2, EP 3.10	storage container to prevent any accidental spills entering the lake.		>
EIA Report	Servicing of any water sports vessels shall be undertaken at suitable facilities away from the artificial lake. In the event that	int that	
5.11.2	fuel or other petroleum products enter the lake, a suitable clean-up plan shall be implemented. The clean-up plan being	ing	7
	devised by the operators of the water recreation centre and approved by EPD prior to the commencement of operations at the	ns at the	>
	water sports centre.		1
	Waste		
EIA Report 5.11.2	 To minimise the potential adverse impacts to aesthetics and odour impacts, the HKITP should maintain floating refuse collection initiatives at both the coast of the Theme Park and within the artificial lake of the Water Recreation Centre. 	Φ	7

Note:

Compliance of mitigation measure	Non-compliance of mitigation measures	Non-compliance but rectified	Not applicable
~	×	•	N/A

APPENDIX C COMPLAINT FLOW DIAGRAM AND COMPLAINT LOG

