

**Public Golf Course at Kau Sai Chau Island, Sai Kung**  
**Operation Phase**  
**Environmental Monitoring & Audit (EM&A) Report**  
**for July 2008**

**(Report No. 382812/0201/005)**

Report Authorized For  
Issue By:



For and on Behalf of  
Black & Veatch Hong Kong Limited

**Black & Veatch Hong Kong Limited**  
25/F, Millennium City 6,  
392 Kwun Tong Road,  
Kowloon, Hong Kong




**The Jockey Club Kau Sai Chau  
Public Golf Course Limited**  
P.O. Box 88,  
Sai Kung Post Office,  
Sai Kung,  
New Territories.

**Aug 2008**

## Table of Content

### Executive Summary

1. Introduction
  - 1.1 *Background of the Project*
  - 1.2 *Purpose of the Report*
  - 1.3 *Structure of the Report*
2. Project Information
  - 2.1 *Background*
  - 2.2 *Site Description*
  - 2.3 *Summary of EM&A Requirements*
3. Environmental Monitoring Requirements
  - 3.1 *Water Quality*
  - 3.2 *Marine Ecology*
  - 3.3 *Landscape and Visual*
  - 3.4 *Soil Nutrient*
4. Monitoring Results
  - 4.1 *Water Quality*
  - 4.2 *Marine Ecology*
  - 4.3 *Landscape & Visual*
  - 4.4 *Soil Nutrient*
5. Conclusions

	<b>Name</b>	<b>Signature</b>	<b>Date</b>
Prepared	<b>Esther Tong</b>		Aug 2008
Checked	<b>Manuel Chua</b>		Aug 2008
Reviewed	<b>PK Lee</b>		Aug 2008

### **List of Figure**

- 1.1 Master Layout Plan of the Proposed Third Golf Course
- 3.1 Proposed Water Quality Monitoring Locations (Operation phase)
- 3.2 Locations of Coral and Seagrass Monitoring (Sites D2, D3 and C)

### **List of Table**

- Table 1.1 Structure of the Report
- Table 2.1 Summary of Impact EM&A Requirements during Operation Phase
- Table 3.1 Derived Summaries of Action and Limit Levels for Freshwater Water Quality
- Table 3.2 Action and Limit Levels for Water Quality Monitoring
- Table 3.3 Derived Summaries of Action and Limit Levels for Marine Water Quality
- Table 3.4 Water Quality Monitoring Parameter, Frequency and Locations
- Table 3.5 Water Quality Monitoring Locations during Operation Phase
- Table 3.9 Analytical Methods to be applied to Water Quality Samples
- Table 4.1-1 Marine Water Exceedance Summary (June to July 2008)
- Table 4.1-2 Fresh water Exceedance Summary (June to July 2008)
- Table 4.1-3 Pesticides Monitoring Results (July 2008)
- Table 4.2-1 Conditions of tagged corals at Site C
- Table 4.2-2 Conditions of tagged corals at Site D2
- Table 4.2-3 Conditions of tagged corals at Control Site

### **List of Annex**

- Annex A Monitoring Programme for the reporting month
- Annex B Event Action Plan
- Annex C Monitoring results
- Annex D Calibration Certificates
- Annex E Fertilizer and pesticides applications

<b>DOCUMENT CONTROL</b>			Public Golf Course at Kau Sai Chau, Sai Kung - Operation Phase	No. 382812/0201/005
<b>AMENDMENT RECORD</b>				Prepared by: Esther Tong
Monthly EM&A Monitoring Report – July 2008			Client: <b>Hong Kong Jockey Club</b>	Initials: ET
				Date: Aug 2008
<b>Pages:</b>	<b>Date:</b>	<b>Issue No.</b>	<b>Description:</b>	<b>Initials:</b>
All	Aug 08	1	Monthly EM&A Report for submission to EPD	ET

## **Executive Summary**

This is the fifth Operation Phase Monthly Environmental Monitoring and Audit (EM&A) Report prepared by Black & Veatch for the Project "Proposed Extension of Public Golf Course at Kau Sai Chau Island, Sai Kung". This report presents the results of the EM&A works conducted in the month of July 2008 (25<sup>th</sup> June to 24<sup>th</sup> July 2008).

### ***Water Quality***

2 sets of water quality monitoring were carried out on 27<sup>th</sup> June and 22<sup>nd</sup> July 2008 at 8 marine and 6 freshwater monitoring locations. No water sample is taken at M\_RO2 (marine station), the monitoring will only be carried out when desalination plant is in operation. For F\_Filter (fresh water station), no filter effluent was discharging during sampling and, thus no water sample was taken on 22<sup>nd</sup> July 2008. Heavy rainstorm events were hoisted on 6<sup>th</sup>, 10<sup>th</sup>, 12<sup>th</sup> and 14<sup>th</sup> July 2008 during this reporting month. Water samples were taken on 7<sup>th</sup>, 10<sup>th</sup>, 13<sup>th</sup> and 15<sup>th</sup> July 2008.

Exceedances found at marine stations are considered non-project related while exceedances found at freshwater stations (Lake 1D, F\_Inland M and F\_Filter) are considered project-related during the reporting month.

### ***Marine Ecology***

Temporary barging point at Kau Sai Chau was completely removed in June 2008. The operation phase coral monitoring was commenced in July 2008. As the construction of the desalination plant intake and outfall at the existing pier was terminated, no dredging work had been carried out during the construction phase. According to the EM&A manual, no coral monitoring was required at Site D2 during the construction phase. As the original baseline coral monitoring at Site D2 was conducted 3.5 years ago (December 2005), most of the tags at the previous tagged corals were lost. Twenty (20) new corals at Site D2 were selected and served as the baseline of the 2-year operation phase coral monitoring.

### ***Landscaping & Visual***

The Contractor is still finalizing the landscaping works, the landscape and visual site audit will be conducted once planting on the golf course are completed. According to the site audit observation, approximate 40-50% compensatory trees have died.

### ***Soil Nutrient***

No soil nutrient analysis was carried out during this reporting month.

## 1. Introduction

### 1.1 Background of the Project

1.1.1 Black & Veatch (hereinafter called the "ET") was appointed by The Jockey Club Kau Sai Chau Public Golf Course Limited (hereinafter called the "Project Proponent") to undertake Operation Phase of Environmental Monitoring and Audit (EM&A) for "Proposed Extension of Public Golf Course at Kau Sai Chau Island, Sai Kung" (hereinafter called the "Project"). Under the requirements of Section 4 of Environmental Permit EP-224/2005/A, EM&A programme as set out in the EM&A Manual is required to be implemented. In accordance with the EM&A Manual, environmental monitoring on water quality, marine ecology, landscape and visual and land contamination during operation phase are required for the Project.

1.1.2 This report summarises the environmental monitoring and audit works for the Project in **July 2008**.

### 1.2 Purpose of the Report

1.2.1 This is the **fifth** EM&A report which summarizes the impact monitoring results and audit findings for the EM&A programme during the reporting period from **25<sup>th</sup> June to 24<sup>th</sup> July 2008**.

### 1.3 Structure of the Report

1.3.1 The structure of the report is shown in Table 1.1.

**Table 1.1 Structure of the Report**

<b>Section</b>		<b>Description</b>
<b>1</b>	Introduction	Details the scope and structure of the report
<b>2</b>	Project Information	Summarizes background and scope of the project and site description
<b>3</b>	Environmental Monitoring Requirement	Summarizes the monitoring parameters, programmes, methodology, frequency, location, action and limit levels, event action plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.
<b>4</b>	Monitoring Results	Summarizes the monitoring results obtained in the reporting period.
<b>5</b>	Environmental Non-conformance	Summarizes any monitoring exceedance, environmental complaints and environmental summons within the reporting period.
<b>6</b>	Conclusions	Provides an overall conclusion of the results and findings of the EM&A programme for the reporting period.

## **2. Project Information**

### **2.1 Background**

2.1.1 The Project comprises the following major components:

- Construction of the third 18-hole public golf course on the east side of the island, south of the existing golfing area;
- A new irrigation lake to collect surface runoff from the new 18-hole golf course. Water stored at the new irrigation lake can also be diverted to existing reservoir for tertiary treatment and recycling;
- A new desalination plant adjacent to the existing pier to serve as an additional irrigation water supply for the new golf course during dry season; and
- Expansion of existing administration and maintenance buildings.

2.1.2 The potential environmental impacts of the Project have been studied in the Environmental Impact Assessment (EIA) report (EIAO Register No. AEIAR- 091/2005). The EIA was approved on 14 November 2005 under the EIAO. An Environmental Permit (EP-224/2005) was granted on 28 November 2005. Application for Variation of an Environmental Permit by the Project Proponent was submitted on 2 August 2006 (Application No. VEP-222/2006) and the EP was superseded by EP-224/2005/A.

### **2.2 Site Description**

2.2.1 A layout plan of the Project is provided in **Figure 1.1**.

### **2.3 Summary of EM&A Requirements**

2.3.1 The EM&A programme requires environmental monitoring for water quality, marine ecology, landscape and visual and land contamination during operation phase. The EM&A requirements for each parameter are described in subsequent sections, including:

- All monitoring parameters;
- Action and Limit Levels for all environmental parameters;
- Event and Action Plans; and
- Environmental mitigation measures, as recommended in the project EIA final report.

2.3.2 A summary of impact EM&A requirements is presented in Table 2.1.

**Table 2.1 Summary of Impact EM&A Requirements during Operation Phase**

<b>Impacts</b>	<b>Parameters/descriptions</b>	<b>Locations</b>	<b>Frequencies</b>
<b>Water Quality</b>	Dissolved Oxygen, Temperature, Turbidity, pH, Salinity, SS, NO <sub>3</sub> -N, NO <sub>2</sub> -N, NH <sub>3</sub> -N, TP, Chl-a and selected pesticides.	9 marine and 6 freshwater locations	2-year of monitoring period for the operation phase. Monitoring should be carried out on bi-weekly basis for the first 12 months, after when the frequency will be reviewed by EPD. Additional monitoring parameters at Lake 1D are required (TKN, Ortho-P and Conductivity)
	Dissolved Oxygen, Temperature, Turbidity, pH, Salinity, SS, NO <sub>3</sub> -N, NO <sub>2</sub> -N, NH <sub>3</sub> -N, TP, Chl-a and selected pesticides.	8 marine locations	Additional water quality monitoring shall be carried out after heavy rain storm or when there is an overflow event from the reservoir, irrigation buffer lake or detention ponds/tanks.
<b>Marine Ecology</b>	Natural corals	Site C, Site D2 and the Control Site.	First three months would be monthly conducted during the first two years of the operation phase. If no exceedance was recorded, the monitoring schedule would be changed to semi-annually, i.e. once in dry season and once in wet season.
<b>Landscape and Visual</b>	Audits to ensure effective implementation of mitigation measures	Golf course area and at visual sensitive receivers	Auditing inspections and reporting shall be undertaken once every two months for the first year of the operation phase.
<b>Soil Nutrient</b>	Nutrient Status of the Soil	Golf course	Twice annually



### 3. Environmental Monitoring Requirements

#### 3.1 Water Quality

##### Monitoring Requirement

3.1.1 Water quality monitoring was conducted in accordance with the EM&A Manual. Tables 3.1 to 3.3 show the established Action/Limit Levels for the water environmental monitoring parameters.

**Table 3.1 Derived Summaries of Action and Limit Levels for Freshwater Water Quality**

Parameters	Location	Action	Location	Limit
DO (mid-depth)		6.3 mg/L	All	4 mg/L ξ
pH (mid-depth)		N/A	All	6.0 - 9.0
SS (mid-depth)	All	3.8 mg/L or 120% of upstream control station's SS at the same tide of the same day	All	8 mg/L or 130% of upstream control station's SS at the same tide of the same day
Turbidity (Tby) (mid-depth)	All	3.1 NTU or 120% of upstream control station's Tby at the same tide of the same day	All	4 NTU or 130% of upstream control station's Tby at the same tide of the same day
Ammonia Nitrogen (mid-depth)		N/A	All	0.01 mg/L
Nitrate Nitrogen (mid-depth)	All	0.10 mg/L	All	0.11 mg/L
Nitrite Nitrogen (mid-depth)		N/A	All	0.01 mg/L
TIN (mid-depth)	All	0.12 mg/L	All	0.13 mg/L
Total Phosphorus (mid-depth)		N/A	All	0.02 mg/L

Remarks:

: Action and limit levels are subjected to review especially for wet season.

Freshwater monitoring locations: F-UA, F-DA, F-UB, F-DB, F-UC, F-DC and F-Inland Marsh

As most of the freshwater samples were reported of NH<sub>3</sub>-N, NO<sub>2</sub>-N levels below the detection limit of 0.01 mg/L, limit level is set at 0.01 mg/L. Similarly for TP, a limit level of 0.02 mg/L (the detection limit of TP) is imposed.

ξ : Water Quality Objectives of the Port Shelter

**Table 3.2 Action and Limit Levels for Water Quality Monitoring  
 (applicable to irrigation lake 1D and existing reservoir)**

Parameter (mg/L unless stated)	Action and Limit Levels
pH	6.0 - 9.0 <sup>(1)</sup>
Turbidity (NTU)	-
Dissolved Oxygen	>4 <sup>(1)</sup>
Chlorophyll a (mg/m <sup>3</sup> )	<5 <sup>(1)</sup>
Nitrate N	0.20 <sup>(1)</sup>
Nitrite N	0.20 <sup>(1)</sup>
Ammoniacal N	0.50 <sup>(1)</sup>
Total Kjeldahl N	1.2 <sup>(2)</sup>
Total Phosphate	0.1 <sup>(1)</sup>
Ortho Phosphate	0.05 <sup>(1)</sup>
Conductivity (µS/cm)	<1000 <sup>(1)</sup>

Note: (1) These values are based on professional judgment and knowledge

(2) Based on 90<sup>th</sup> percentile of operational phase monitoring data (1996 to June 1998)

**Table 3.3 Derived Summaries of Action and Limit Levels for Marine Water Quality**

Parameters	Location	Action	Location	Limit
<b>DO (Surface &amp; Middle)</b>	FCZ	6.0 mg/L	FCZ	5.3 mg/L
	All except FCZ	4.9 mg/L	All except FCZ	4.6 mg/L
<b>DO (Bottom)</b>	All	3.7 mg/L	All	3.4 mg/L
<b>pH (depth-averaged)</b>		N/A	All	6.5 - 8.5
<b>SS (Depth-averaged)</b>	FCZ	4.5 mg/L	FCZ	5.6 mg/L
	All except FCZ	6.1 mg/L	All except FCZ	10.6 mg/L
<b>SS (Depth-averaged) Dredging for submarine pipelines</b>	M_RO1	6.1 mg/L	M_RO1	10.6 mg/L
<b>Turbidity (Tby) (depth-averaged)</b>	FCZ	2.9 NTU $\alpha$	FCZ	3.9 NTU $\alpha$
	All except FCZ	3.3 NTU $\alpha$	All except FCZ	6.2 NTU $\alpha$
<b>Ammonia Nitrogen (depth-averaged)</b>	FCZ	0.02 mg/L	FCZ	0.03 mg/L
	All except FCZ	0.05 mg/L $\Delta$	All except FCZ	0.05 mg/L $\Delta$
<b>Nitrate Nitrogen (depth-averaged)</b>	FCZ	0.08 mg/L	FCZ	0.09 mg/L
	All except FCZ	0.09mg/L $\Delta$	All except FCZ	0.09 mg/L $\Delta$
<b>Nitrite Nitrogen (depth-averaged)</b>	FCZ	0.02 mg/L $\theta$	FCZ	0.02 mg/L $\theta$
	All except FCZ	0.02 mg/L	All except FCZ	0.04 mg/L
<b>TIN (depth-averaged)</b>	FCZ	0.12 mg/L	FCZ	0.14 mg/L
	All except FCZ	0.16 mg/L	All except FCZ	0.18 mg/L
<b>Total Phosphorus (depth-averaged)</b>	All	0.09 mg/L $\Delta$	All	0.09 mg/L $\Delta$

Remarks:

: Action and limit levels are subjected to review especially for wet season throughout the construction phase of the project.

: Action and limit levels are subjected to review before the dredging works.

⊗ : All are based on EM&A baseline monitoring data due to marked difference between EPD turbidity data and those from the baseline survey.

Δ : For nutrient monitoring (except NO<sub>2</sub>-N) at non-FCZ stations, the trigger level has made reference to the existing golf course guideline values. The guideline value of NO<sub>2</sub>-N is below the current detection limit of 0.01mg/L and thus not used.

θ : The same action and limit level of 0.02 mg/L is determined from the EM&A baseline data as 78% of the NO<sub>2</sub>-N data are ≤ 0.01 mg/L and all remaining 22% equal to 0.02 mg/L.

**FCZ** including fish culture zones of Kai Lung Wan, Tai Tau Chau and Kau Sai

**All except FCZ** including remaining impact monitoring station of M\_RO1, M\_Marsh, M\_BP and M\_Coral.

Control monitoring locations: M\_A & M\_B

### Monitoring Parameters, Frequency and Programme

- 3.1.2 For marine water quality, measurements shall be taken at both mid-flood and mid-ebb tides and at three water depths (1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth is less than 6 m, in which case the mid-depth station may be omitted). Should the water depth be less than 3 m, only the mid-depth station will be monitored.
- 3.1.3 For the stream course, measurements shall be taken at mid-water depth.
- 3.1.4 The water quality parameters which need to be monitored are as follows:
- Marine water quality - dissolved oxygen (DO), temperature, turbidity, suspended solids (SS), pH and salinity
  - Freshwater water quality - dissolved oxygen (DO), temperature, turbidity, suspended solids (SS), pH, salinity and conductivity (Lake 1D only).
- 3.1.5 Additional marine and freshwater water quality monitoring parameters for the impact monitoring during construction include nitrate nitrogen (NO<sub>3</sub>-N), nitrite nitrogen (NO<sub>2</sub>-N), ammonia nitrogen (NH<sub>3</sub>-N), total phosphate (TP) and selected pesticides. For Lake 1D, Total Kjeldahl Nitrogen (TKN) and Orthophosphate (Ortho P) are required.
- 3.1.6 Additional water quality monitoring at Tai Tau Chau FCZ (TTC), Kai Lung Wan FCZ (KLW), Kau Sai FCZ (KS), downstream of the existing marsh (M\_Marsh), marine water of Port Shelter (M\_Coral), existing reservoir (F\_Inland M) and Control stations (M\_A and M\_B) shall be carried out after heavy rain storm or when there is an overflow event from the reservoir, irrigation buffer lake or detention ponds/tanks. The heavy rain storm shall be defined when there is an amber/red/black rainstorm warning signal issued by the Hong Kong Observatory. The water sample shall be taken within 24 hours after the black/red/amber rainstorm warning signal is cancelled. Please refer to revised EM&A manual for the sampling condition requirement after a heavy rain storm event occurs. The monitoring parameters shall include dissolved oxygen, temperature, turbidity, suspended solids, pH and salinity. Additional parameters shall be the same as stated in paragraphs 3.1.5.

*Monitoring Frequency*

3.1.7 After reviewing the water quality monitoring results during construction phase and early operation phase, EPD<sup>1</sup> agreed to revise monitoring parameters and frequency are summarized in Table 3.4. The monitoring programme for the reporting period is shown in **Annex A**.

**Table 3.4 Water Quality Monitoring Parameter, Frequency and Locations**

Parameters	Location	Frequency	Sampling Depth
Dissolved Oxygen (mg/L)	<p><b>Marine Water</b> Fish culture zone stations: TTC, KLW, KS</p> <p>Control stations: M_A, M_B</p> <p>Impact stations: M_RO1, M_RO2, M_Marsh, M_Coral</p> <p><b>Freshwater Water</b> Stream A (F_DA) Stream B (F_DB) Stream C (F_DC) Inland Marsh (F_Inland_M) Filter System (F_Filter) Irrigation Lake 1D (F_lake 1D)</p>	<p><b>Bi-weekly</b></p> <p><u>Marine water</u> : 2 times per day – 1 for mid-flood and 1 for mid-ebb</p> <p><u>Freshwater</u> : Mid-depth per trip</p>	3 individual water depth samples (surface, middle & bottom)
Temperature (°C)			
Turbidity (NTU)			
pH			
Salinity (ppt)			
Suspended Solids (mg/L)			
Nutrients <sup>2</sup>			
Chemicals <sup>3</sup>	<p><b>Monthly (wet season) and Bi-Monthly (dry season)</b></p> <p><u>Marine water</u> : 2 times per day – 1 for mid-flood and 1 for mid-ebb</p> <p><u>Freshwater</u> : Mid-depth per trip</p>	1 composite sample (combine surface, middle and bottom) with replicate	

Wet season: Apr to October; Dry season: November to March

<sup>1</sup> EPD letter dated 14 July 2008 (Ref. no.: (6) in EP2/N8/O/47 Ax(7) Pt X) regarding the approval on the revised water quality monitoring proposal.

<sup>2</sup> Ammonia Nitrogen, Nitrate Nitrogen, Nitrite Nitrogen, Total Inorganic Nitrogen, Total Phosphorus and Chlorophyll a. For Lake 1D, addition nutrient parameters are Total Kjeldahl Nitrogen, Ortho Phosphate and Conductivity (µS/cm).

<sup>3</sup> Pesticides (approved lists are Imazaquin, Glyphosate, Oxadiazon, 2,4-D/Mecoprop, Chlorothalonil, Mancozeb, Iprodione, Fosetyl Aluminum, Chlorpyrifos, Fipronil and Imidachloprid).

### Monitoring Locations

3.1.8 The water quality monitoring locations for marine and freshwater (**Figure 3.1**) are summarized in Table 3.5.

**Table 3.5 Water Quality Monitoring Locations during Operation Phase**

Identification Number	Location	Approx. Water Depth	No. of Depth
<i>Marine Water (9 stations)</i>			
TTC	Tai Tau Chau Fish Culture Zone	9.5 m	3
KLW	Kai Lung Wan Fish Culture Zone	13 m	3
KS	Kau Sai Fish Culture Zone	11 m	3
M_BP	Temporary barging point	9.6 m	3
M_RO1	Desalination plant south of the existing pier	5 m	2
M_RO2	Desalination plant south of the existing pier	13 m	3
M_Marsh	Discharge point at the existing marsh	7.7 m	3
M_Coral	Marine water of Port Shelter	10.2m	3
M_A	Water Control Station of Port Shelter	7.5 m	3
M_B	Water Control Station of Port Shelter	16.5 m	3
<i>Fresh Water (7 stations)</i>			
F_DA	downstream of stream A	Mid-depth	1
F_DB	downstream of stream B	Mid-depth	1
F_DC	downstream of stream C	Mid-depth	1
F_Inland M	Downstream of the existing marsh (Inland)	Mid-depth	1
F_lake 1D	Irrigation Lake 1D	Mid-depth	1
F_Filter	Filter effluent point at Holes 5 / 6	Mid-depth	1

### Monitoring Equipment

#### *Dissolved Oxygen and Temperature Measuring Equipment*

3.1.9 The instrument shall be a portable and weatherproof DO measuring instrument complete with cable and sensor, and use a DC power source. The equipment shall be capable of measuring:

- dissolved oxygen levels in the range of 0 - 20 mg L<sup>-1</sup> and 0 - 200% saturation; and
- a temperature of 0 - 45 degrees Celsius.

3.1.10 It shall have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables shall be available for replacement where necessary. (For example, YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).

- 3.1.11 Should salinity compensation not be built-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

*Turbidity Measurement Instrument*

- 3.1.12 Turbidity shall be measured in situ by the nephelometric method. The instrument shall be portable and weatherproof turbidity measuring instrument using a DC power source complete with cable, sensor and comprehensive operation manuals. It shall have a photoelectric sensor capable of measuring turbidity between 0 - 1000 NTU (for example, Hach model 2100P or an approved similar instrument). The cable shall not be less than 25m in length. The meter shall be calibrated in order to establish the relationship between NTU units and the levels of suspended solids.

*Suspended Solids*

- 3.1.13 A water sample at least 2.5L in capacity with messenger and using a 10m line should be collected. Samples should be submitted to HOKLAS accredited laboratory as soon as possible for gravimetric analysis for suspended.

*Sampler*

- 3.1.14 A water sampler is required. It shall comprise a transparent PVC cylinder, with a capacity of not less than 2 litres, which can be effectively sealed with latex cups at both ends. The sampler shall have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (for example, Kahlsico Water Sampler or an approved similar instrument).

*Water Depth Detector*

- 3.1.15 A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be hand held or affixed to the bottom of the work boat, if the same vessel is to be used throughout the monitoring programme.

*Salinity*

- 3.1.16 A portable salinometer capable of measuring salinity in the range of 0 - 40 parts per thousand (ppt) shall be provided for measuring salinity of the water at each monitoring location.

*pH*

- 3.1.17 The instrument shall consist of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It shall be readable to 0.1pH in a range of 0 to 14. Standard buffer solutions of at least pH 7 and pH 10 shall be used for calibration of the instrument before and after use. Details of the method shall comply with APHA, 19th ed. 4500-HTB.

*Flow Rate Meter*

- 3.1.18 A portable, battery-operated flow meter should be used for the determination of water depth at each designated monitoring location and record in m<sup>3</sup>/s. A hand held or meter fixed to the underside of the survey boat may be used.

#### *Sample Containers and Storage*

- 3.1.19 Water samples for laboratory analysis shall be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen) and delivered to the laboratory and analysed as soon as possible after collection. Sufficient volume of samples shall be collected to achieve the required detection limit.

#### *Monitoring Position Equipment*

- 3.1.20 A hand-held or boat-fixed type digital Differential Global Positioning System (DGPS) with way point bearing indication or other equipment instrument of similar accuracy, shall be provided and used during marine water monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

#### Monitoring Methodology and Calibration Details

- 3.1.21 Dissolved oxygen (DO), temperature, turbidity, pH and salinity were measured in situ at the designated water quality monitoring stations. General observation, weather conditions, with the sampling time, date and location were marked on the field record sheet.
- 3.1.22 Water samples were taken from each monitoring station for laboratory analysis. The sample identification number, sampling location, date, time, project name and analyses were required.
- 3.1.23 The samples were placed in a cooler with ice (to 4°C without being frozen) and kept away from sunlight. Samples were submitted to a Hong Kong Laboratory Accreditation Scheme (HOKLAS) or other international accredited laboratory for analysis within 24 hours of sampling.

#### *Calibration of In-Situ Instruments*

- 3.1.24 All in situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use and subsequently re-calibrated at three monthly intervals throughout all stages of the water quality monitoring programme. Responses of sensors and electrodes were checked with certified standard solutions before each use. Wet bulb calibration for a DO meter were carried out before measurement at each monitoring location.

#### *Laboratory Analysis*

- 3.1.25 All laboratory work were carried out by ALS Technichem Pty Ltd (HOKLAS accredited laboratory). Water samples were collected at the monitoring and control stations for carrying out the laboratory determinations. The determination work will start within 24 hours after collection of the water samples. The analysis shall follow the standard methods according to APHA Standard Methods for the Examination of Water and Wastewater, 19th Edition, or an equivalent method approved by EPD.

**Table 3.9 Analytical Methods to be applied to Water Quality Samples**

<b>Determinant</b>	<b>Standard Method</b>	<b>Reporting Limit</b>
Suspended Solids	APHA 2540 D	2 mg/L
Nitrate Nitrogen	APHA 4500-NO <sub>3</sub> <sup>-</sup>	0.01 mg/L
Nitrite Nitrogen	APHA 4500-NO <sub>2</sub> <sup>-</sup>	0.01 mg/L
Ammonia Nitrogen	APHA 4500-NH <sub>3</sub> (D)	0.01 mg/L
Total phosphorus	ASTM D515-88B	0.02 mg/L*

Determinant	Standard Method	Reporting Limit
Chlorophyll a	APHA 10200 H2 &3	0.5 µg/L

Remarks: \*After review baseline data, the detection limit report will be revised to 0.02 mg/L.

### *QA/QC Procedure*

- 3.1.26 ALS Technichem Pty Ltd. has comprehensive quality assurance and quality control programmes. For QA/QC procedures of parameters, one duplicate sample was analysed for every batch of 20 samples as required by HOKLAS.

### Event and Action Plans

- 3.1.27 The Event and Action Plan (EAP) for water quality monitoring is presented in **Annex B**.

## **3.2 Marine Ecology**

### Introduction

- 3.2.1 The marine ecological monitoring surveys are conducted in accordance with the EM&A manual.
- 3.2.2 As stipulated in the EM&A Manual, the ecological monitoring surveys for marine ecology included coral monitoring at both the eastern (Site C) and western (Site D2) coasts of Kau Sai Chau Island and Control Site. The purpose of the monitoring survey was to check the conditions of the tagged corals and the sites.

### Monitoring Frequency and Schedule

- 3.2.3 At each of the Site C and a Control Site near the AFCD's Coral Buoy at Sharp Island (**Figure 3.2**), 20 natural coral colonies are already selected and tagged during construction phase. If the tagged coral is found die or not suitable for sequent operation phase monitoring during the first month survey, new coral will be selected, tagged and replaced for the damage one. The species of corals had been tagged included the following 15 species: *Cyphastrea xerailia*, *Favia speciosa*, *Favites abdita*, *Favites pentagona*, *Goniastrea aspera*, *Goniopora columna*, *Hydnophora exesa*, *Leptastrea pruinosa*, *Lithophyllon undulatum*, *Pavona decussata*, *Platygyra acuta*, *Platygyra carnosus*, *Plesiastrea versipora*, *Psammocora superficialis*, and *Turbinaria peltata*. As the construction of the desalination plant intake and outfall at the existing pier was terminated, no dredging work had been carried out during the construction phase. According to the EM&A manual, no coral monitoring was required at Site D2 during the construction phase. As the original baseline coral monitoring at Site D2 was conducted 3.5 years ago (December 2005), most of the tags at the previous tagged corals were lost. Twenty (20) new corals were selected in Site D2 for operation phase monitoring purposes. The species of corals selected in Site D2 included the following 10 species: *Acropora tumida*, *Cyphastrea serailia*, *Favia speciosa*, *Favites chinensis*, *Goniastrea aspera*, *Goniopora columna*, *Gonipora stutchburyi*, *Pavona decussata*, *Porties lobata*, and *Turbinaria peltata*. The operation phase coral monitoring covering Site D2, Site C and the Control Site.
- 3.2.4 The coral monitoring will be conducted monthly for the first three months of the operation phase, and if no exceedance was recorded, the monitoring schedule will be changed to semi-annually (i.e. one dry season and one in wet season) during the rest of the operation phase. Monitoring survey will consist of checking tagged corals at both impact sites and control site. Percentages of survival, sedimentation and bleaching for each tagged corals will be recorded. The monitoring programme for the reporting period is shown in **Annex A**.



### Event and Action Plans

3.2.5 The Event and Action Plan (EAP) for ecology monitoring is presented in **Annex B**.

### **3.3 Landscape and Visual**

3.3.1 The EIA concluded that the landscape and visual impacts associated with the construction of the third golf course are anticipated to be acceptable with mitigation. In order to ensure that the effective management and implementation of landscape mitigation measures developed and defined in the EIA, regular site inspections on trees health will be conducted. Auditing inspections and reporting are undertaken once every two months during the first year of the operation phase. The monitoring programme for the reporting period is shown in **Annex A**.

### **3.4 Soil Nutrient**

3.4.1 Routine soil testing for nutrients at East Course will be conducted semi-annually to ensure that nutrient applications to the golf course are having the desired effect. Adjustments, if necessary, are made to the applications program approved by Golf Course Superintendent to amend any soil imbalances or deficiencies in nutrients. The details of the fertilizers and pesticides application will also be recorded.

#### 4. Monitoring Results

4.1.1 Monitoring data are provided in **Annex C**.

#### 4.1 Water Quality

4.1.2 Marine and freshwater water quality monitoring were conducted at the 9 and 6 designated monitoring stations respectively.

4.1.3 Application of the discharge licence of the desalination plant is in progress. The monitoring M\_RO2 is not necessary until the desalination plant fully is operational.

4.1.4 Monitoring of marine and freshwater locations was conducted on 2 occasions in June and July 2008 (27<sup>th</sup> June and 22 July 2008). The QA/QC results for laboratory testing in the reporting month are acceptable and summarised in **Annex D**. Rainstorm signal was hoisted on 6<sup>th</sup>, 10<sup>th</sup>, 12<sup>th</sup> and 14<sup>th</sup> July 2008 during this reporting month. Water samples were taken on 7<sup>th</sup>, 10<sup>th</sup>, 13<sup>th</sup> and 15<sup>th</sup> July 2008.

4.1.5 As there is no water discharge from the Holes 5 / 6 through the drainage system during sampling, no water sample for F\_Filter was collected during the reporting month. Summary of fertilizer and pesticides applications are summarized in **Annex E**.

4.1.6 Chemical applications were applied during the reporting month. They are approved pesticides listed in the turfgrass management plan in the final EIA report. Water samples were required to send to overseas laboratory for analysis and testing.

##### Marine water

4.1.7 The marine water exceedance is summarised in **Table 4.1-1**.

4.1.8 SS exceedance recorded at KS was 5.2 mg/L on 22<sup>nd</sup> July 2008 which had similar SS concentration measured at M\_B (4 mg/L). The SS exceedance is considered non-project related.

**Table 4.1-1 Marine Water Exceedance Summary (June to July 2008)**

Monitoring Location	Exceedance Level	Date	Parameters	Project-related
KS	Action Level	22 July 2008	SS	No

##### Fresh water

4.1.9 The fresh water exceedances are summarised in **Table 4.1-2**.

**Table 4.1-2 Fresh water Exceedance Summary (June to July 2008)**

Monitoring Location	Exceedance Level	Date	Parameters	Project-related
F_DA	Limit Level	27 June 2008	NO <sub>3</sub> -N, TIN	No
	Action Level	7 July 2008	SS	No
	Limit Level	7 July 2008	NO <sub>3</sub> -N, TIN	No
	Action Level	15 July 2008	SS	No
	Action Level	22 July 2008	SS	No
F_DB	Action Level	27 June 2008	SS	No

Monitoring Location	Exceedance Level	Date	Parameters	Project-related
	Limit Level	27 June 2008	NO <sub>3</sub> -N, TIN	No
	Limit Level	7 July 2008	NO <sub>3</sub> -N, TIN	No
	Action Level	22 July 2008	SS	No
F_DC	Limit Level	27 June 2008	NO <sub>3</sub> -N, TIN	No
	Limit Level	7 July 2008	NO <sub>3</sub> -N, TIN	No
F_Inland M	Limit Level	27 June 2008	Turbidity, SS, NO <sub>3</sub> -N, TIN, TP, Chl a	Yes
	Limit Level	7 July 2008	Turbidity, SS, NO <sub>3</sub> -N, TIN, TP	Yes
	Limit Level	9 July 2008	Turbidity, SS, NO <sub>3</sub> -N, TIN, TP, Chl a	Yes
	Limit Level	10 July 2008	Turbidity, SS, NH <sub>3</sub> -N, NO <sub>3</sub> -N, TIN	Yes
	Limit Level	13 July 2008	Turbidity, SS, NH <sub>3</sub> -N, NO <sub>3</sub> -N, TIN, TP	Yes
	Limit Level	15 July 2008	Turbidity, SS, NO <sub>3</sub> -N, TIN	Yes
	Limit Level	22 July 2008	NO <sub>3</sub> -N, TIN, TP, Chl a	Yes
F_Filter	Action Level	27 June 2008	Turbidity	Yes
	Limit Level	27 June 2008	NO <sub>3</sub> -N, TIN, TP	Yes
	Action Level	7 July 2008	SS	Yes
	Limit Level	7 July 2008	NO <sub>3</sub> -N, TIN, TP	Yes
	Limit Level	9 July 2008	NO <sub>3</sub> -N, TIN, TP, Chl a	Yes
	Limit Level	10 July 2008	NO <sub>3</sub> -N, TIN, TP	Yes
	Action Level	13 July 2008	SS	Yes
	Limit Level	13 July 2008	NO <sub>3</sub> -N, TIN, T P	Yes
	Limit Level	15 July 2008	NO <sub>3</sub> -N, TIN, TP, Chl a	Yes
Lake 1D	Limit Level	27 June 2008	Turbidity, TP	Yes
	Limit Level	7 July 2008	Turbidity, NO <sub>3</sub> -N, TP	Yes
	Limit Level	9 July 2008	Turbidity, TP	Yes
	Limit Level	10 July 2008	Turbidity, TP	Yes
	Limit Level	13 July 2008	Turbidity, TP	Yes
	Limit Level	15 July 2008	Turbidity, TP	Yes
	Limit Level	22 July 2008	TP	Yes

- 4.1.10 Action level turbidity exceedances were recorded at downstream A and B (4 to 5 mg/L). It is considered non-project related and mainly due to disturbance of stream after rainstorm events occurred.
- 4.1.11 Water quality of the streams before any commencement works were measured in April 2006 in order to indicate natural variation between dry and wet seasons. By taking into account the seasonal variation (wet season) together with the baseline monitoring data (dry season), the 95%-ile and 99%-ile for NO<sub>3</sub>-N are 0.22 and 0.55 mg/L respectively while the 95%-ile and 99%-ile for TIN are 0.25 and 0.67 mg/L respectively.
- 4.1.12 Limit levels nitrate nitrogen (NO<sub>3</sub>-N) and total inorganic nitrogen (TIN) exceedances were recorded at downstream A, B & C. NO<sub>3</sub>-N concentrations ranging from 0.13 mg/L to 0.27 mg/L while TIN concentrations ranging from 0.15 mg/L to 0.29 mg/L. Both NO<sub>3</sub>-N and TIN concentrations are well within the wet season natural variation range. Therefore, it is considered that all exceedances are non-project related.
- 4.1.13 Low values of chlorophyll a exceedances (0.7 to 0.9 µg/L) were recorded at downstream of Fresh Water Inland Marsh. Continue exceedances for NO<sub>3</sub>-N (0.12 to 0.25 mg/L), TIN (0.14

to 0.43 mg/L) and TP (0.03 to 0.08 mg/L) were recorded at Fresh Water Inland Marsh (F\_Inland Marsh) and ADS Filter (F\_Filter) during July 2008, all of them are considered project related. Further study on the water quality will be carried out. Review of the nutrients application may be required.

- 4.1.14 The lake 1D is designed for temporary storage to collect the runoff from East Course through the closed low flow drainage system. The water will be recycled and reused as one of the irrigation water sources for the East Course. NO<sub>3</sub>-N, TIN, ortho-phosphate and chlorophyll a exceedances were recorded. As there is no overflow / discharge from the Lake 1D to marine or fresh water bodies, no further action has to be taken.
- 4.1.15 The monitoring of pesticides are summarised in **Table 4.1-3**. All applied pesticides were below detection limit.

**Table 4.1-3 Pesticides Monitoring Results (July 2008)**

Date	Monitoring Station	Parameters	Monitoring Result
27 <sup>th</sup> June 08	Fosetyl Aluminum : M_Marsh, TTC, M_BP, M_Coral, KS, F_DA, F_DB, F_DC, F_Inland_Marsh, F_Filter	Imidacloprid	Undetectable
27 <sup>th</sup> June 08	Mancozeb : M_Marsh, TTC, M_BP, M_Coral, KS, F_DA, F_DB, F_DC, F_Inland_Marsh, F_Filter	Chlorothalonil	Undetectable
22 <sup>nd</sup> July 08	M_Marsh, TTC, M_BP, M_Coral, KS, F_DA, F_DB, F_DC, F_Inland_Marsh	Iprodione	Undetectable
22 <sup>nd</sup> July 08	M_Marsh, TTC, M_BP, M_Coral, KS, F_DA, F_DB, F_DC, F_Inland_Marsh	Chlorpyrifos	Undetectable

## 4.2 Marine Ecology

- 4.2.1 The removal of the temporary barging point was completed in June 2008. The operation phase monitoring commenced in July 2008. The July 08 monitoring covering Site D2, Site C and the Control Site served as the baseline for the operation phase.
- 4.2.2 The present Marine Ecological Monitoring Survey was conducted on 6<sup>th</sup> July 2008. The weather conditions were windy but clear on the survey day, the underwater visibility was also good (approximately 3m).
- 4.2.3 At Site C and the Control Site, the twenty (20) colonies of natural corals selected during the Baseline Survey were checked for conditions, while at Site D2, 20 new corals were selected for the purposes of the operation phase monitoring. Some corals in Site C and the Control Site were found missing, probably due to the wave actions. Replacement coral colonies will be selected in next coral survey to maintain the number of tagged corals in each site to be 20.
- 4.2.4 Site C was on the south-eastern coast of Kau Sai Chau Island and had a high coral coverage among the sites investigated during the EIA Study. The sizes of coral colonies at Site C were also larger than those at other sites. Site C was away from the boundary of the new golf course and would not be subject to direct impacts during construction. The site and its vicinity still remained similar conditions as during the Baseline Survey. Among the 20 tagged corals in Site C, C-04 and C-20 were found missing. C-04 had been previously destroyed by adverse weather during the construction phase (this had been reported in previous construction phase monitoring report.). C-20 could still be recovered in the last construction phase monitoring survey in December 2007, and thus might be affected by weather conditions and typhoons in the last few months. Replacement coral colonies will be selected in next monitoring survey. For other

recovered corals, no mortality or sedimentation was found (see **Table 4.2-1** and **Annex C - Photo Plates 4.2-1 to 4.2-2**).

- 4.2.5 Site D2 is close to the desalination plant. The monitoring site was not within area to be directly impacted by the project, but was located about 80m to the south of the existing ferry pier, where an area of hard substrates (bedrock and boulders) was present. The seabed was covered by bedrock. The bedrock cover continued to over 100m south from the pier. It was estimated that less than 5% coverage of corals on the bedrock area, but the sizes of those colonies were fairly large (some reach 30cm). 20 natural corals were selected during the baseline survey in December 2005 (with codes ranging from D-01 to D-20). The distribution of these selected corals ran along the contour of the bedrock, rather than parallel with the coastline as most natural corals occurred along the bed rock edge. The species of corals newly selected in Site D2 included the following 10 species: *Acropora tumida*, *Cyphastrea serailia*, *Favia speciosa*, *Favites chinensis*, *Goniastrea aspera*, *Goniopora columna*, *Gonipora stutchburyi*, *Pavona decussata*, *Porties lobata*, and *Turbinaria peltata*. The conditions, mortality, sedimentation and bleaching of these 20 corals were shown in **Table 4.2-2** and **Annex C - Photo Plates 4.2-3 to 4.2-4**.
- 4.2.6 The occurrence of seagrasses at Site D2 and Site D3 were checked. No seagrasses were found at Site D2, but an area of about 50m x 50m at Site D3 was found colonized by *Halophila* sp. The conditions of the seagrasses at Site D3 were fair given the summer high temperature and the recent freshwater flush from significant rainfall in June.
- 4.2.7 The Control Site is the buoy of coral marker established by AFCD in Sharp Island. Similar with Site C, both the coral coverage percentage and the sizes of coral colonies were high at this site and would not be impacted by the Project. The site and its vicinity still remained similar conditions as during the Construction Phase Monitoring. Coral X-05 was lost in previous construction phase monitoring in June 2006. Replacement coral for X-05 will be selected in next monitoring survey. The remaining 19 tagged corals were recovered. The corals remained similar conditions as during the construction phase monitoring (**Annex C - Photo Plates 4.2-5 to 4.2-6**). No mortality, sedimentation or bleaching was found on any of the tagged corals (see **Table 4.2-3**).
- 4.2.8 **Photo Plates 4.2-1 to 4.2-6** showed the photos of each tagged corals. The assigned numbers, species, mortality percentage, sedimentation coverage percentage and bleaching percentage of the baseline conditions of tagged corals and their present conditions were presented in **Tables 4.2-1 to 4.2-3** below.

**Table 4.2-1 Conditions of tagged corals at Site C**

Code of tagged corals	Species	Baseline Survey (July 2008)		
		Mortality (%)	Sedimentation (%)	Bleaching (%)
C-01	<i>Platygyra carnosus</i>	0	0	0
C-02	<i>Platygyra carnosus</i>	0	0	0
C-03	<i>Favia speciosa</i>	0	0	0
C-04*	<i>Favites abdita</i>	Missing	Missing	Missing
C-05	<i>Turbinaria peltata</i>	0	0	0

Code of tagged corals	Species	Baseline Survey (July 2008)		
		Mortality (%)	Sedimentation (%)	Bleaching (%)
C-06	<i>Favia speciosa</i>	0	0	0
C-07	<i>Platygyra acuta</i>	0	0	0
C-08	<i>Platygyra acuta</i>	0	0	0
C-09	<i>Favia speciosa</i>	0	0	0
C-10	<i>Platygyra acuta</i>	0	0	0
C-11	<i>Favia speciosa</i>	0	0	0
C-12	<i>Platygyra acuta</i>	0	0	0
C-13	<i>Platygyra carnosus</i>	0	0	0
C-14	<i>Favia speciosa</i>	0	0	0
C-15	<i>Goniopora columna</i>	0	0	0
C-16	<i>Platygyra carnosus</i>	0	0	0
C-17	<i>Goniopora columna</i>	0	0	0
C-18	<i>Platygyra carnosus</i>	0	0	0
C-19	<i>Favites pentagona</i>	0	0	0
C-20*	<i>Favia speciosa</i>	Missing	Missing	Missing

\*Replacement corals will be selected in next monitoring survey

**Table 4.2-2 Conditions of tagged corals at Site D2**

Code of tagged corals	Species	Baseline Survey (July 2008)		
		Mortality (%)	Sedimentation (%)	Bleaching (%)
D-01	<i>Goniopora columna</i>	0	0	0
D-02	<i>Goniastrea aspera</i>	0	0	0
D-03	<i>Favia speciosa</i>	0	0	0
D-04	<i>Favia speciosa</i>	0	0	0
D-05	<i>Goniastrea aspera</i>	0	0	0
D-06	<i>Goniastrea aspera</i>	0	0	0
D-07	<i>Goniopora stutchburyi</i>	0	0	0
D-08	<i>Turbinaria peltata</i>	0	0	0
D-09	<i>Goniastrea aspera</i>	0	0	0
D-10	<i>Goniastrea aspera</i>	0	0	0
D-11	<i>Favia speciosa</i>	0	0	0
D-12	<i>Turbinaria peltata</i>	0	0	0
D-13	<i>Turbinaria peltata</i>	0	0	0
D-14	<i>Favites chinensis</i>	0	0	0
D-15	<i>Porites lobata</i>	0	0	0
D-16	<i>Turbinaria peltata</i>	0	0	0
D-17	<i>Acropora tumida</i>	0	0	0
D-18	<i>Cyphastrea serailia</i>	0	0	0
D-19	<i>Cyphastrea serailia</i>	0	0	0
D-20	<i>Pavonna descussata</i>	0	0	0

**Table 4.2-3 Conditions of tagged corals at Control Site**

Code of tagged corals	Species	Baseline Survey (July 2008)		
		Mortality (%)	Sedimentation (%)	Bleaching (%)
X-01	<i>Platygyra carnosus</i>	0	0	0
X-02	<i>Platygyra carnosus</i>	0	0	0
X-03	<i>Platygyra carnosus</i>	0	0	0
X-04	<i>Pavona decussata</i>	0	0	0
X-05*	<i>Hydnophora exesa</i>	Missing	Missing	Missing
X-06	<i>Platygyra carnosus</i>	0	0	0
X-07	<i>Platygyra carnosus</i>	0	0	0
X-08	<i>Favites abdita</i>	0	0	0
X-09	<i>Cyphastrea serailia</i>	0	0	0
X-10	<i>Cyphastrea serailia</i>	0	0	0
X-11	<i>Platygyra carnosus</i>	0	0	0
X-12	<i>Platygyra acuta</i>	0	0	0
X-13	<i>Platygyra acuta</i>	0	0	0
X-14	<i>Platygyra acuta</i>	0	0	0
X-15	<i>Platygyra acuta</i>	0	0	0
X-16	<i>Platygyra acuta</i>	0	0	0
X-17	<i>Favia speciosa</i>	0	0	0
X-18	<i>Platygyra acuta</i>	0	0	0
X-19	<i>Goniastrea aspera</i>	0	0	0
X-20	<i>Cyphastrea serailia</i>	0	0	0

\*Replacement corals will be selected in next monitoring survey

### 4.3 Landscape & Visual

4.3.1 The landscape work is not yet completed by the Contractor. The operation phase monitoring will commence when the Final Landscape Plan is available from the Contractor.

### 4.4 Soil Nutrient

4.4.1 No soil nutrient was taken and reported during this reporting month.

## **5. Conclusions**

- 5.1.1 The Environmental Monitoring and Audit (EM&A) Report presents the operational EM&A works undertaken during the period from 25<sup>th</sup> June to 24<sup>th</sup> July 2008 in accordance with EM&A Manual and the requirement under EP-224-2005/A.
- 5.1.2 Exceedances on marine stations are recorded and considered non-project related. The exceedances are mainly due to the natural variation.
- 5.1.3 Exceedances on fresh water stations are recorded and considered non-project related for Streams A, B and C (F\_DA, F\_DB and F\_DC). The exceedances are mainly due to wet season variation. For exceedances records measured at F\_Inland Marsh, F\_Filter and Lake 1D, it is considered project- related. Further study on the water quality will be carried out. Review of the nutrients application may be required.
- 5.1.4 Application of discharge licence of the desalination plant is in progress. Marine water monitoring location at M\_RO2 is not required.
- 5.1.5 Baseline of the coral monitoring at Site C, Site D and Control Site were conducted in July 2008. Three subsequent monthly coral monitoring in the August, September and October 2008 will be conducted.
- 5.1.6 Removal of rock-filled pier at the temporary barging point was completed in June 2008. Coral monitoring was carried out in July 2008. No coral damage was recorded.
- 5.1.7 The landscape work is not yet completed by the Contractor. The operation phase monitoring will commence when the Final Landscape Plan is available from the Contractor.
- 5.1.8 No environmental complaint / summon was received during the reporting month.



# **Annex A**

## **Monitoring Programme for the reporting month**

<b>June 2008</b>						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			25	26	27 WQ	28
29	30					

<b>July 2008</b>						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4	5
6	7 RWQ	8	9	10 RWQ	11	12
13 RWQ	14	15 RWQ	16	17	18	19 ME
20	21	22 WQ	23	24	25	26
27	28	29	30	31		

WQ: Water Quality Monitoring (WQ); Rainstorm Water Sampling (RWQ)  
 ME: Marine Ecology

# **Annex B**

## **Event Action Plan**

### **Event and Action Plan for Water Quality**

Should monitoring results of the water quality parameters at any designated monitoring station exceed the water quality criteria related to turf management, action the proposed actions to be taken shall be as follows:

- inform Golf Course Manager immediately and stop chemical application;
- notify EPD and AFCD;
- review the application and re-evaluate suitability and availability of alternatives to chemical controls, etc.;
- agree remedial measures with Golf Course Manager and inform EPD and AFCD;
- implement the agreed remedial measures immediately; and
- increase monitoring frequency and/or locations to demonstrate effectiveness of the remedial measures.

**Action and Limit level and Event Action Plan for natural corals monitoring**


<b>Parameters</b>	<b>Action Level</b>	<b>Limit Level</b>
Sedimentation	a 15% increase in the percentage of sedimentation on the hard corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites	a 25% increase in the percentage of sedimentation on the hard corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites
Bleaching	a 15% increase in the percentage of bleaching of hard corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites	a 25% increase in the percentage of bleaching of hard corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites
Mortality	a 15% increase in the percentage of partial mortality of corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites	a 25% increase in the percentage of partial mortality of corals occurs at more than 20% of the tagged coral colonies at one or more monitoring sites

<b>Action</b>	<b>Action Level</b>	<b>Limit Level</b>
Operation phase	If the Action Level is exceeded the ET Leader should inform Golf Course Operator, EPD, and AFCD. The data from the water quality monitoring should also be reviewed. If the water quality monitoring shows no attributable effects of the installation works, then the Action Level is not triggered. If the water quality data indicate exceedances (salinity and/or pesticides) the ET Leader should discuss with the Golf Course Operator the most appropriate method of reducing salinity (e.g. reduce the daily operation time of the desalination plant), and/or control chemicals from runoff (e.g. reduce the frequency and quantity of chemical applied, check the intactness and effectiveness of the closed drainage system and stream buffer zone). This mitigated method should then be enacted on the next working day.	If the Limit Level is exceeded the ET Leader should inform all parties Golf Course Operator, EPD, and AFCD immediately. Should the Limit Level be exceeded, the Golf Course Operator should stop the operation of the desalination plant and/or the application of chemicals immediately and work out the solution according to the requirements of EPD and AFCD. The operation of the desalination plant and/or the application of chemicals would be suspended until an effective solution is identified.


# **Annex C**


## **Monitoring results**


# Water Quality

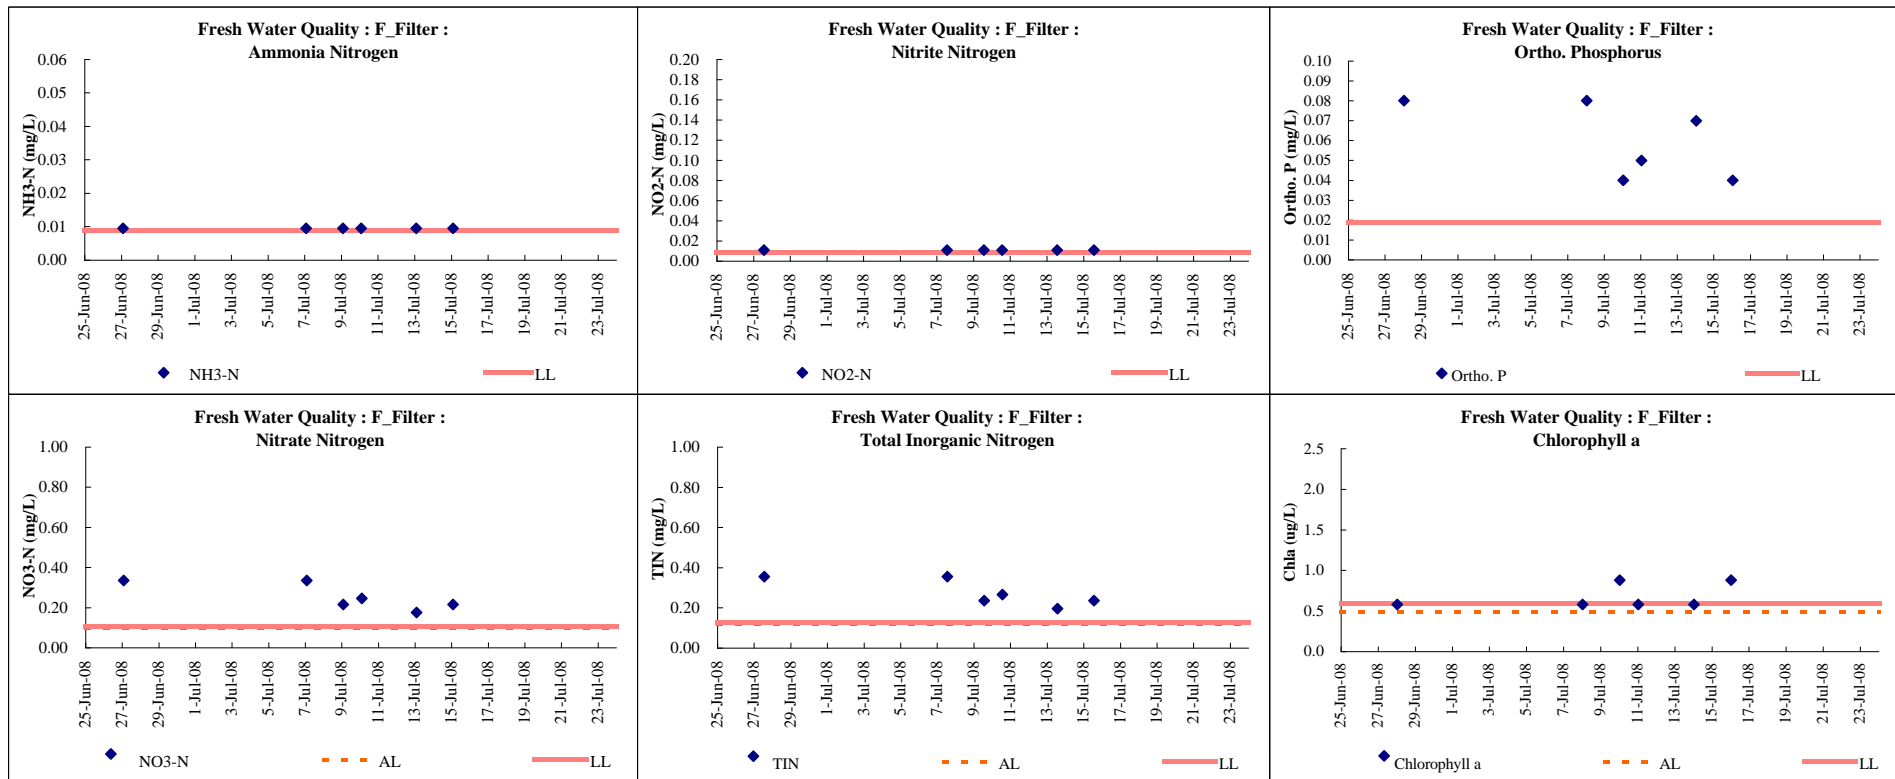





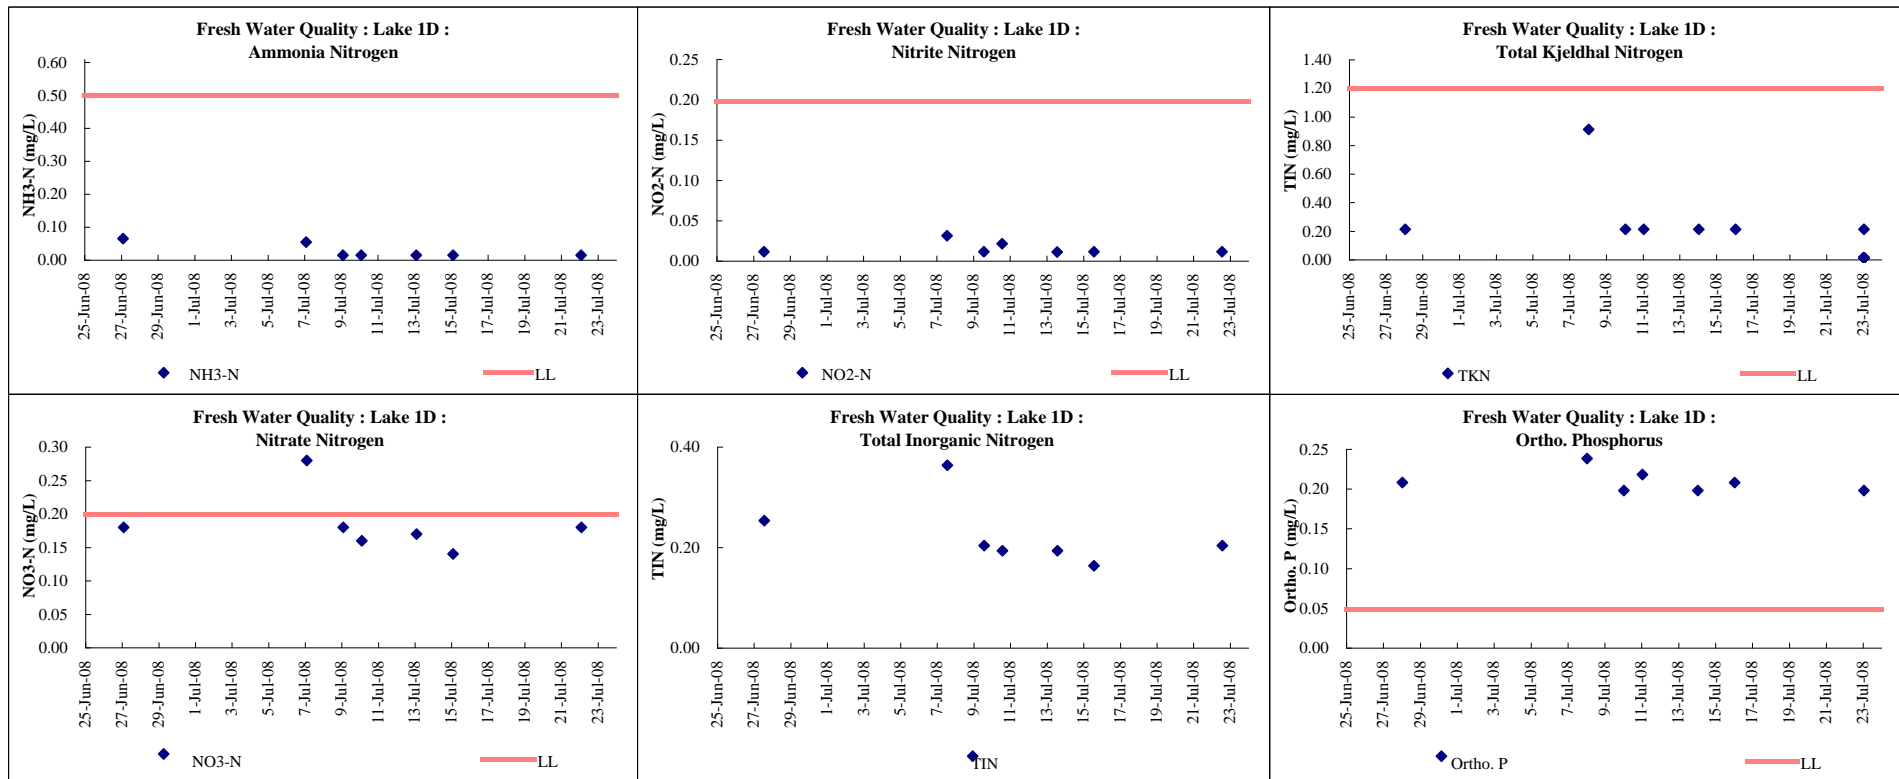


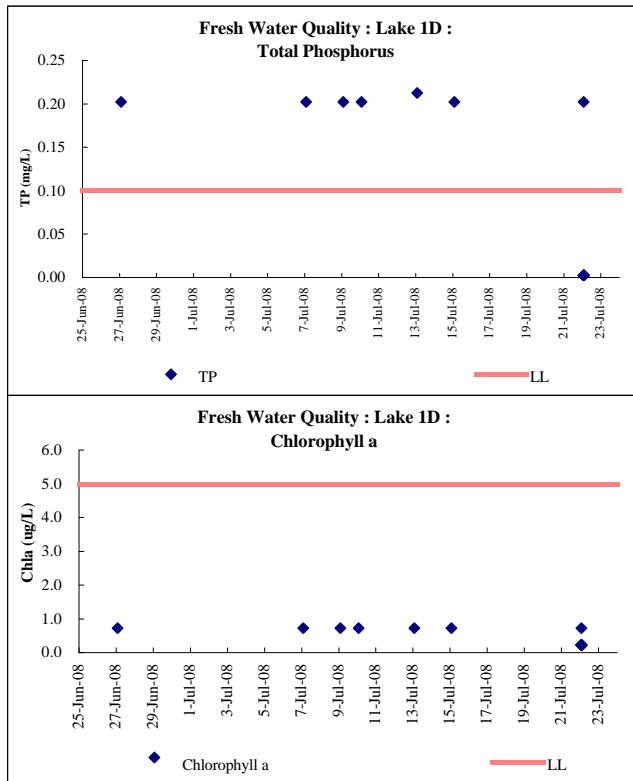


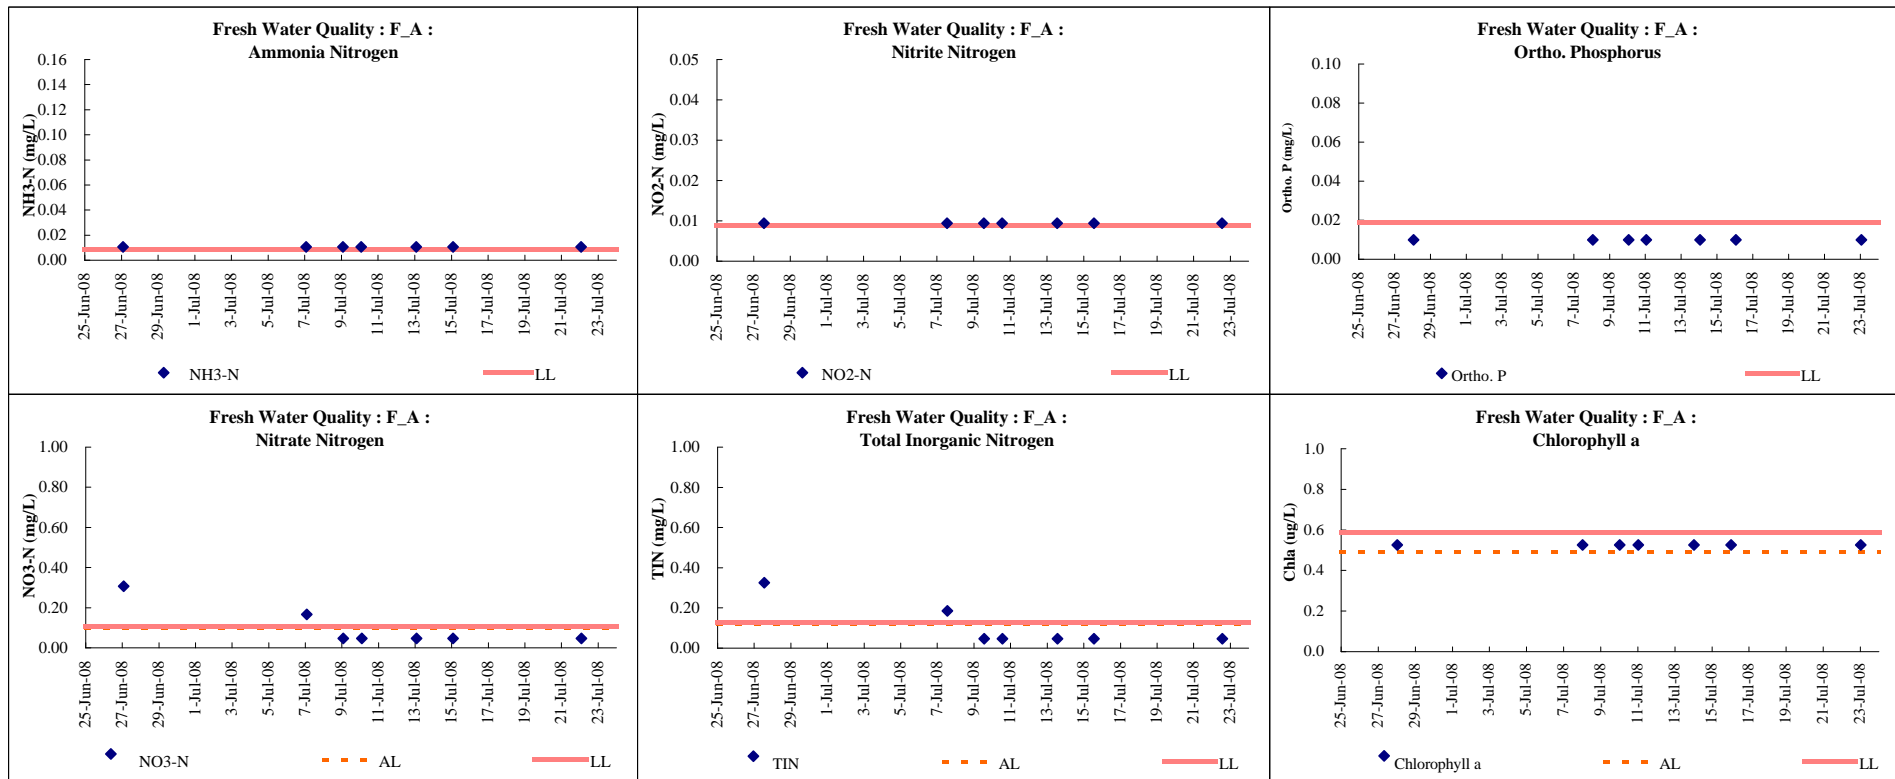


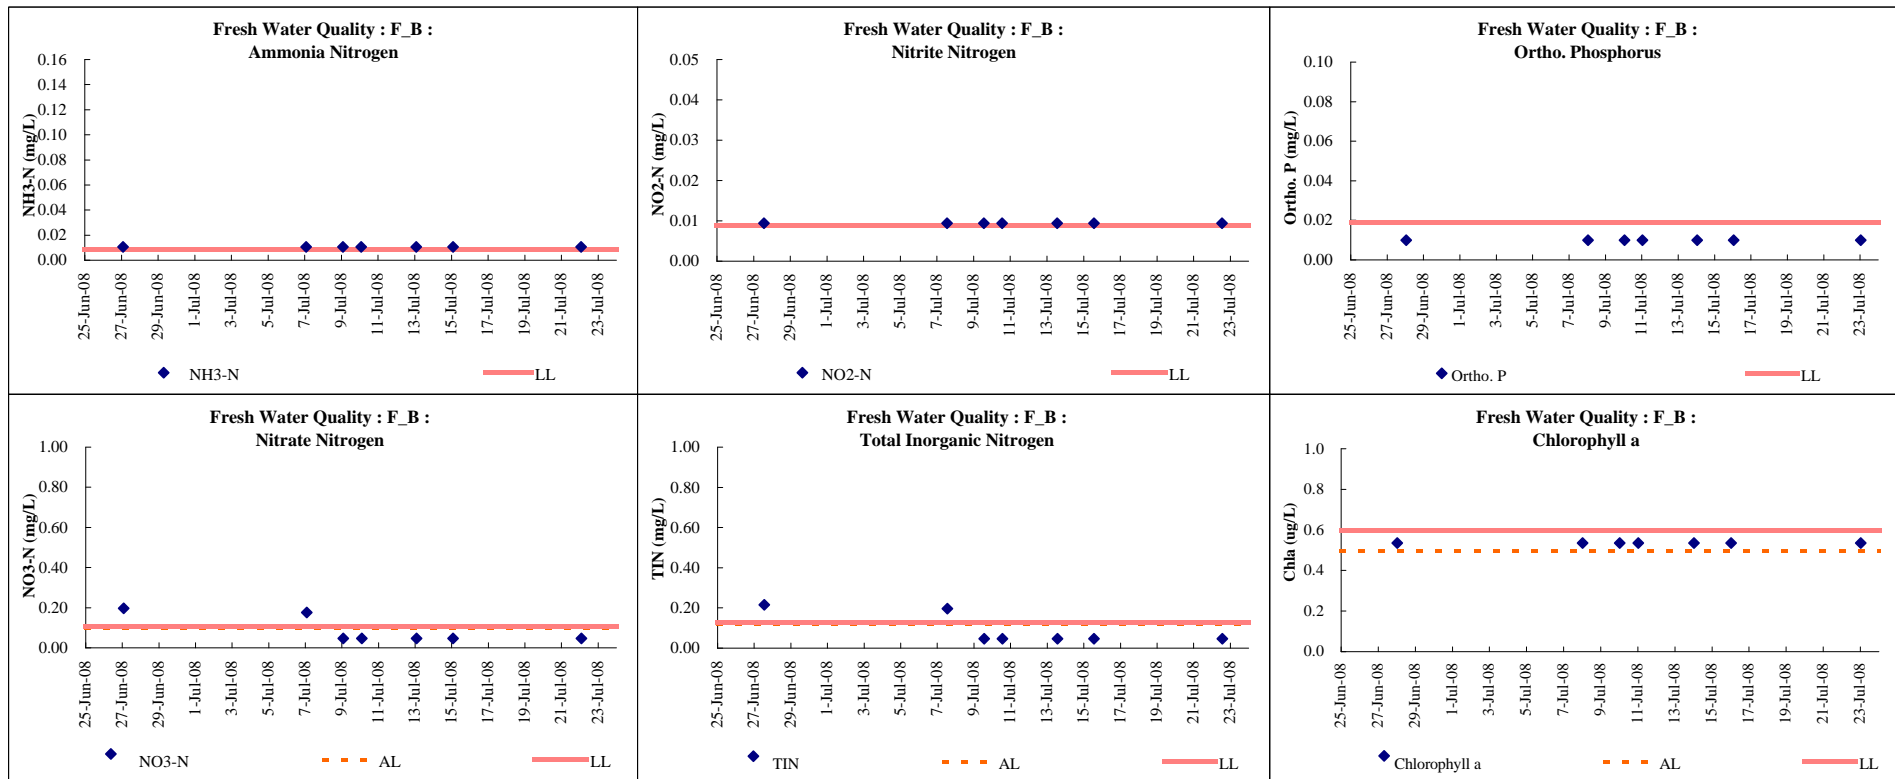

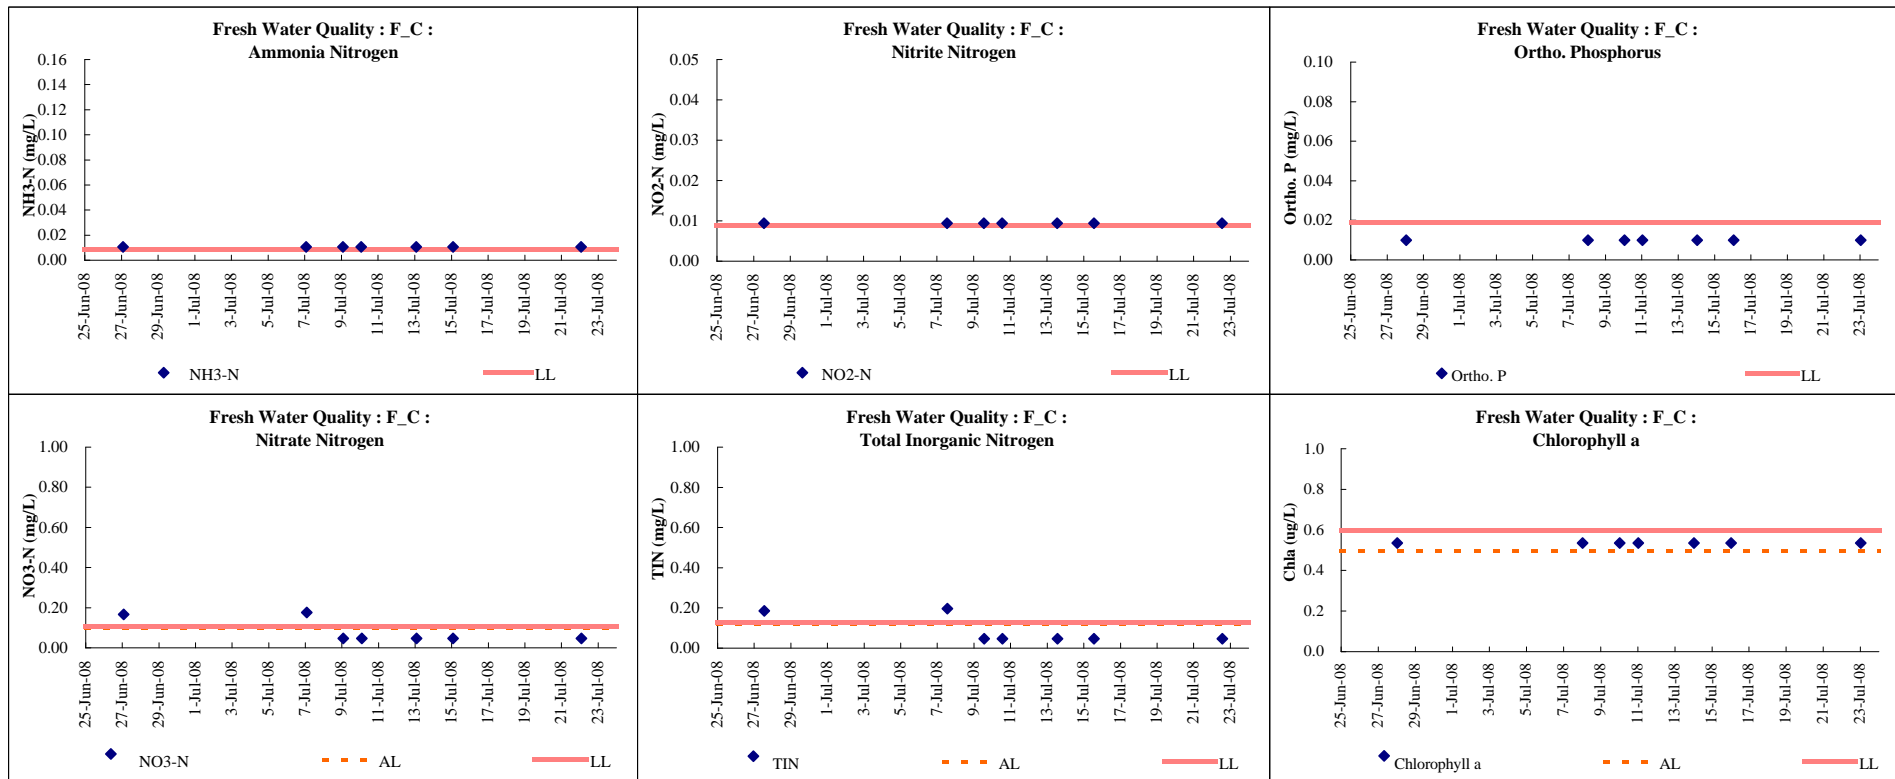


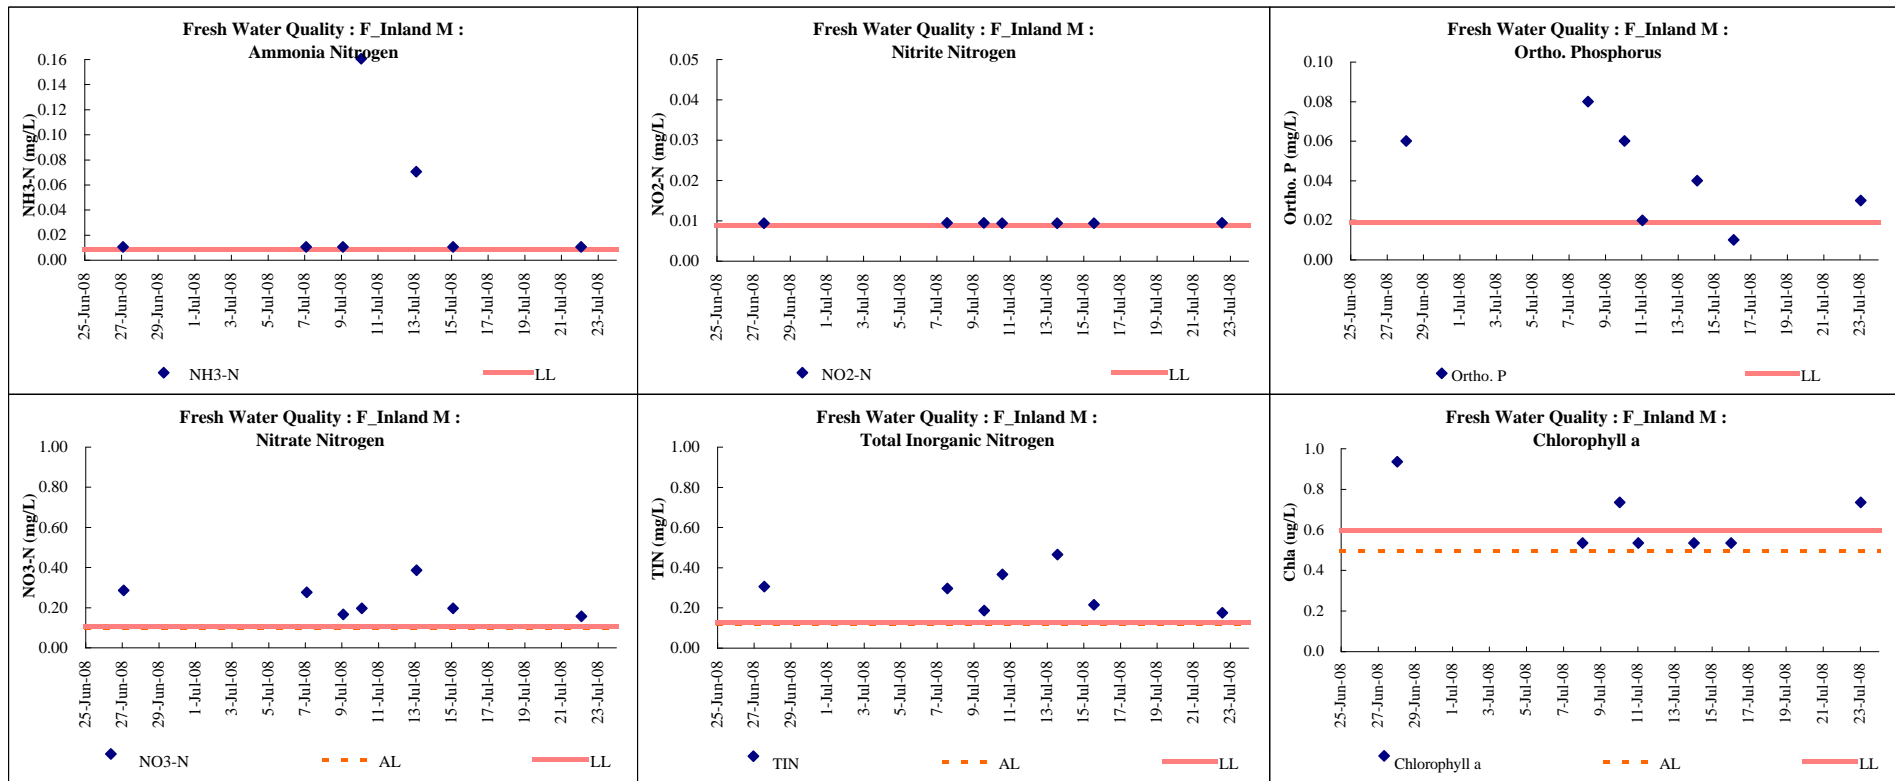


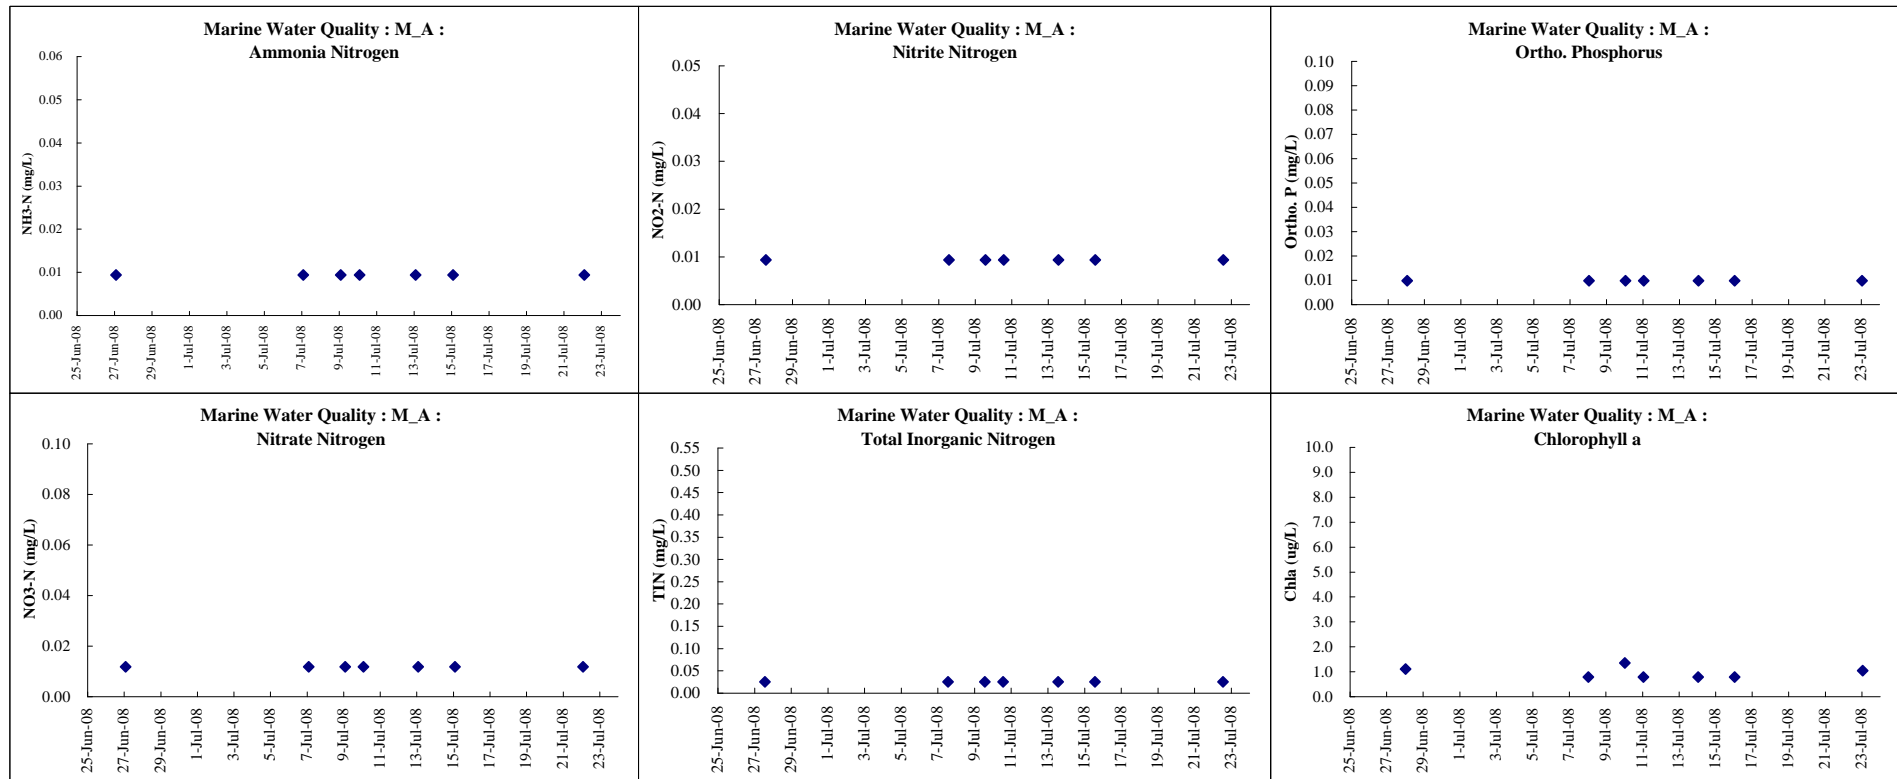


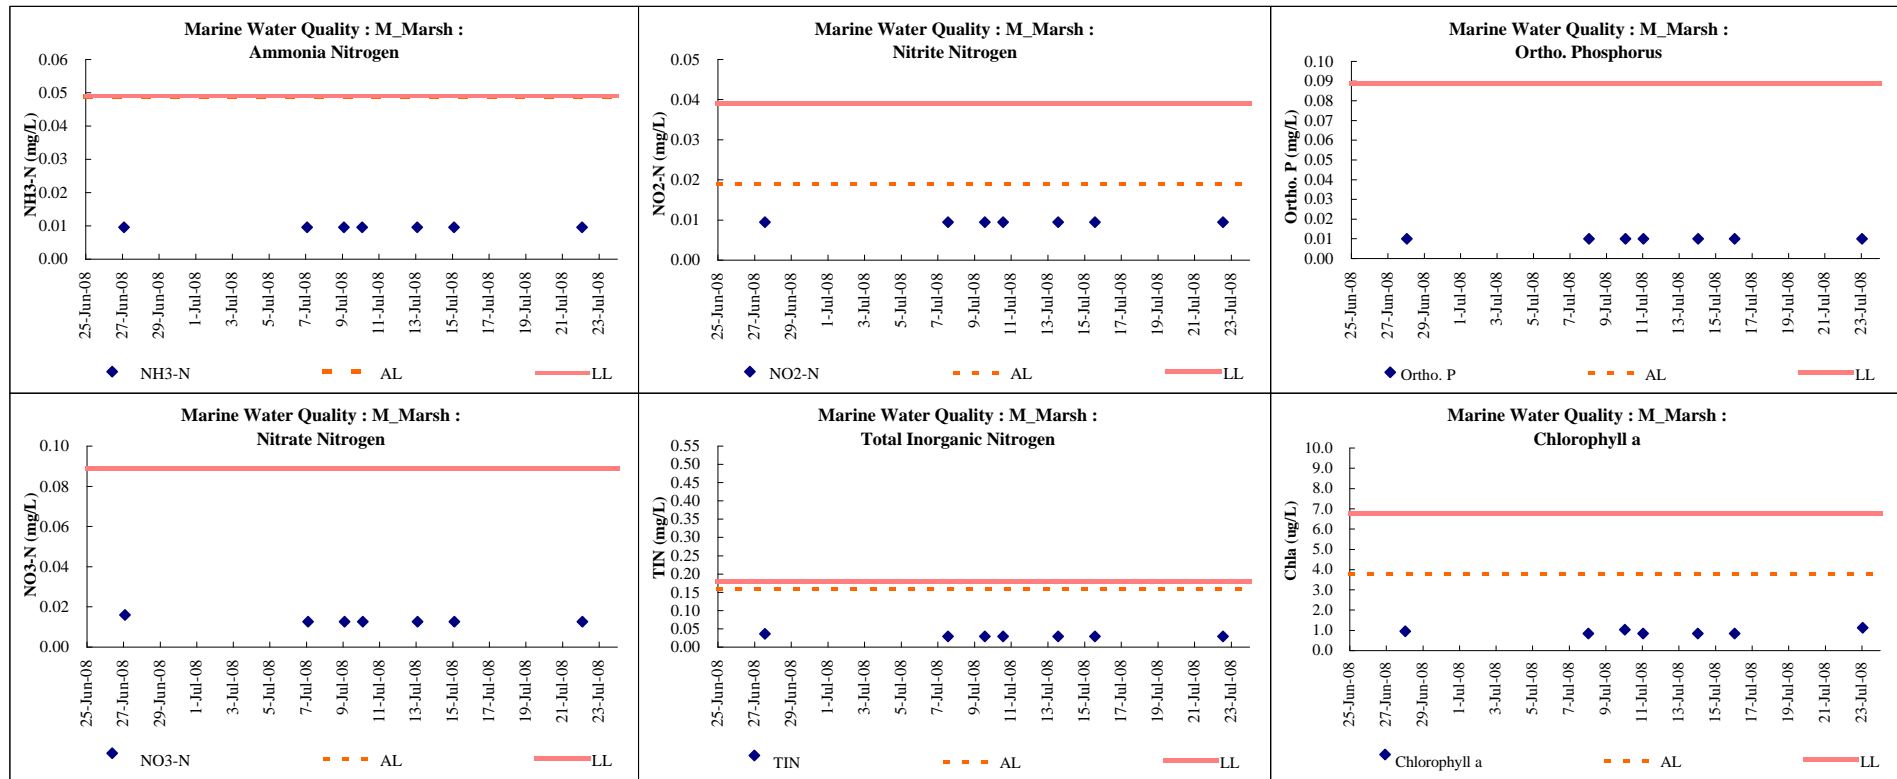





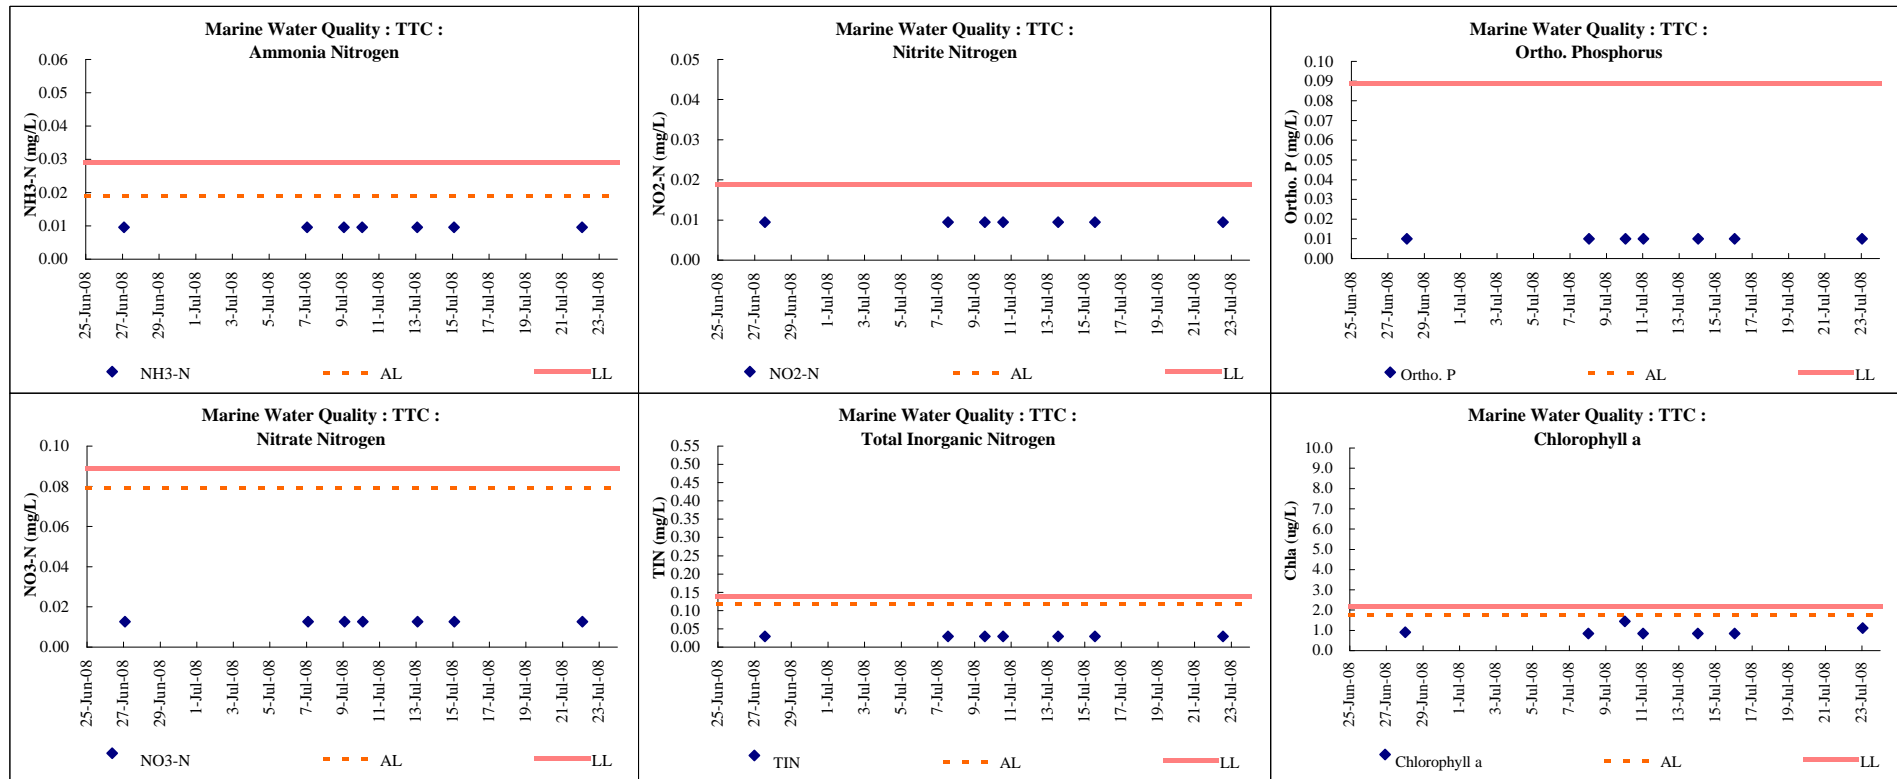


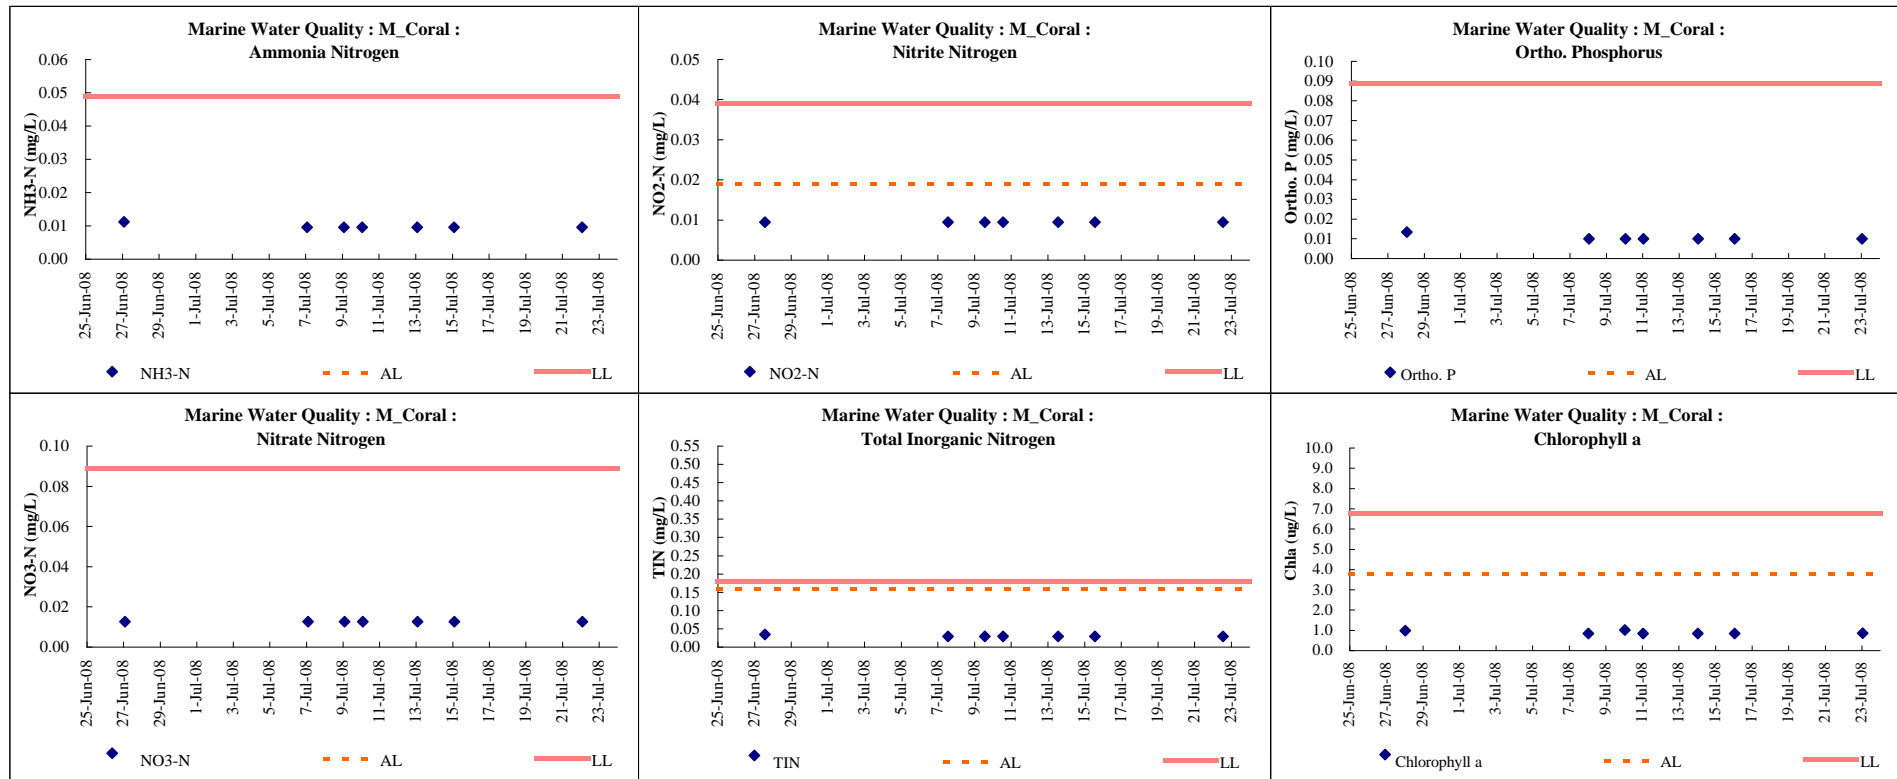


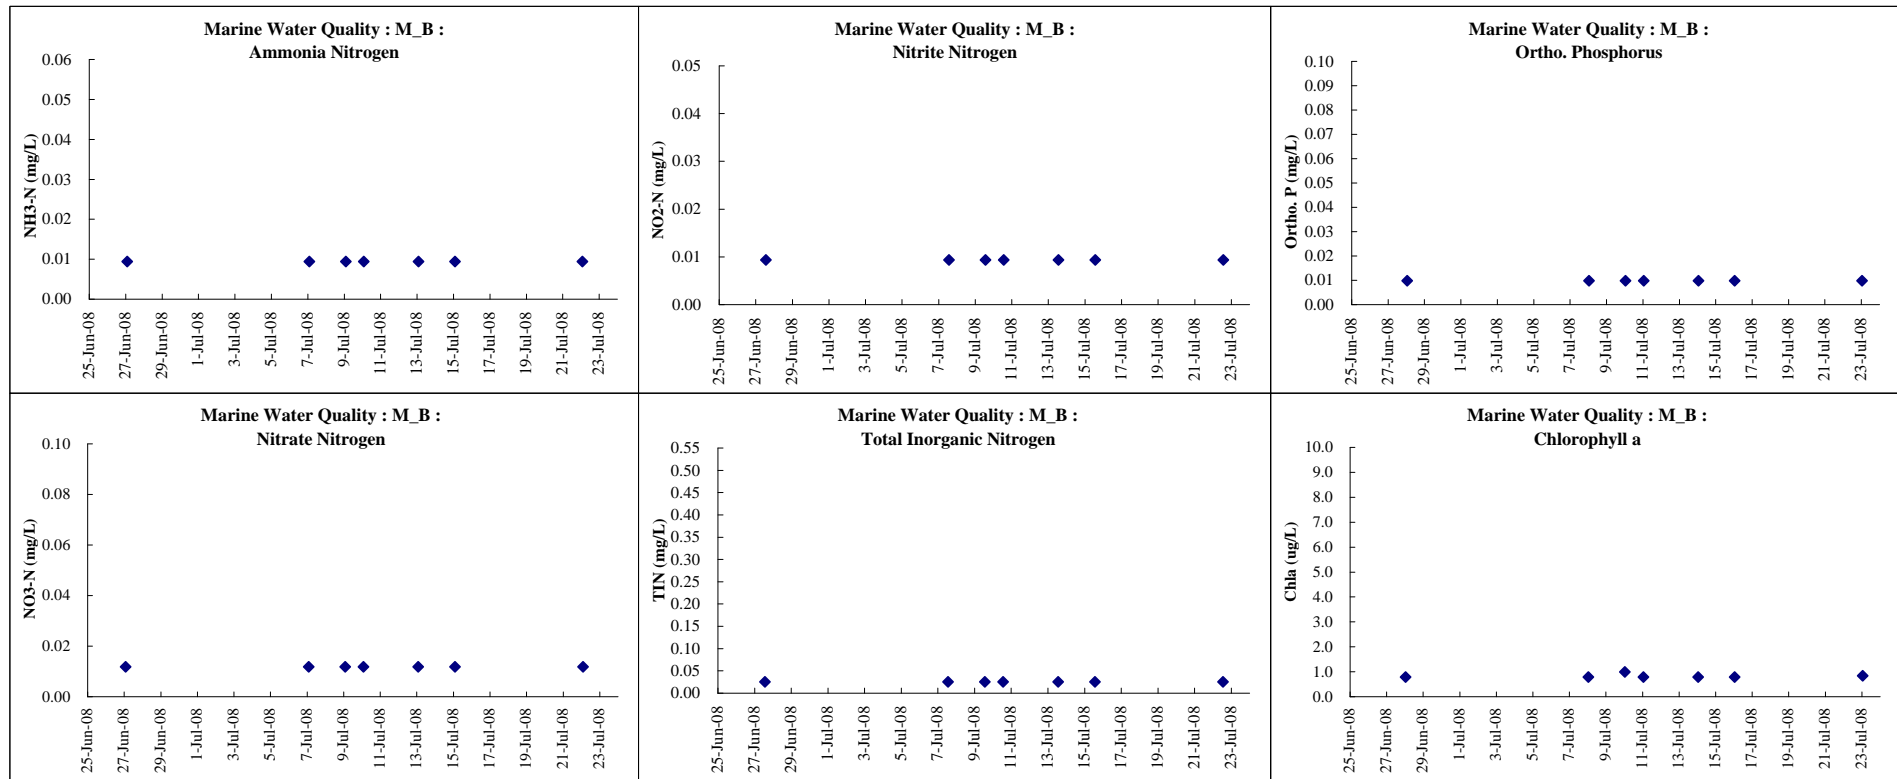


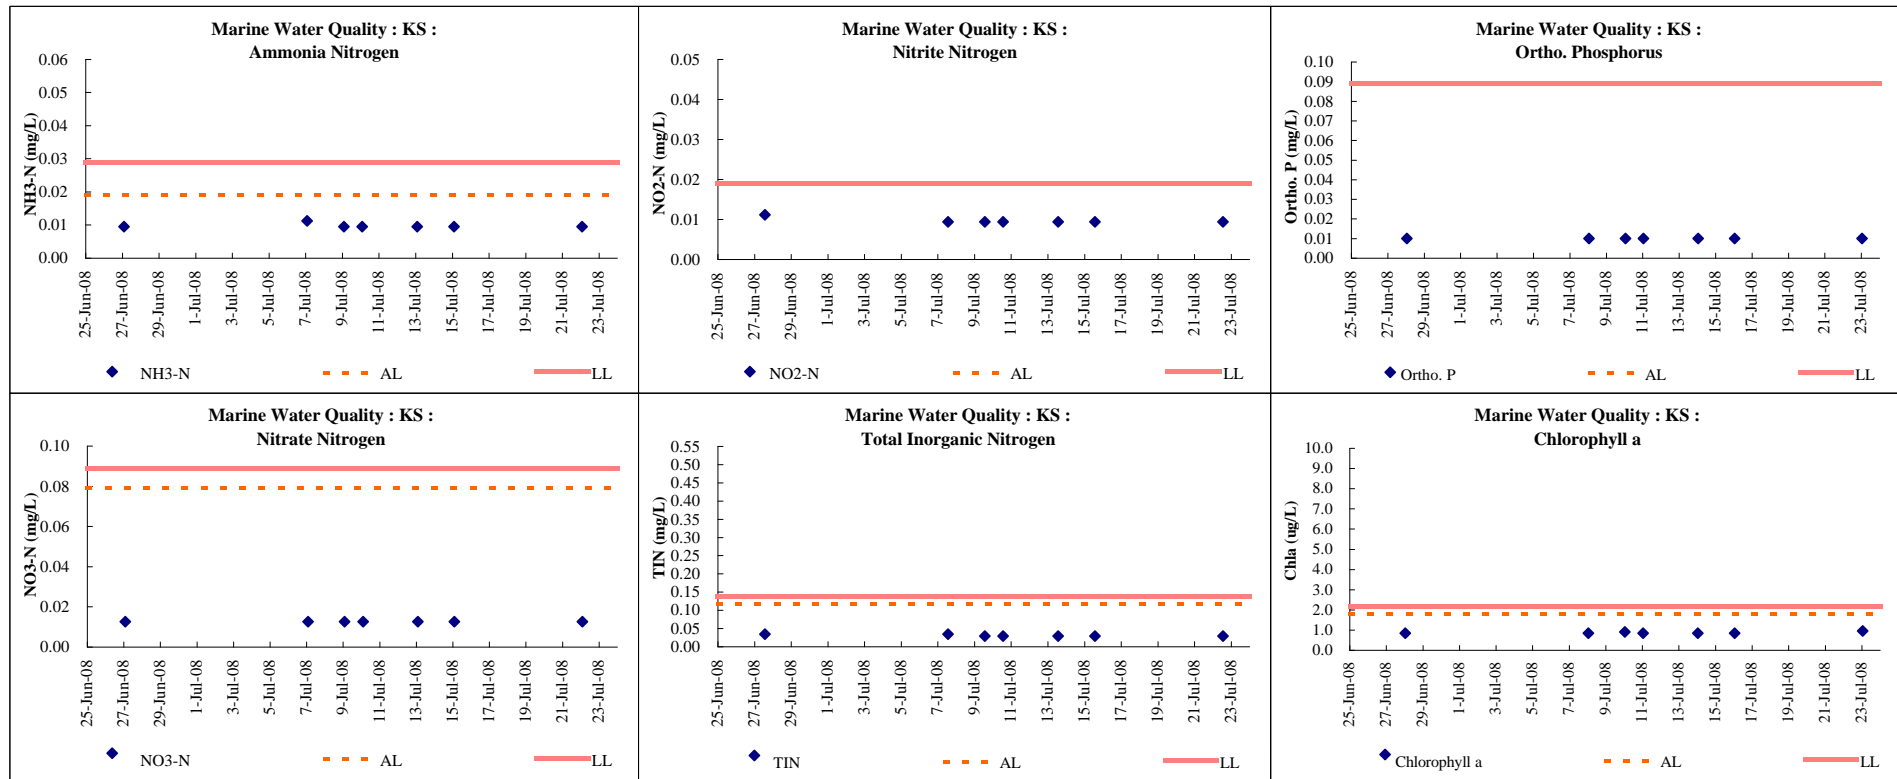

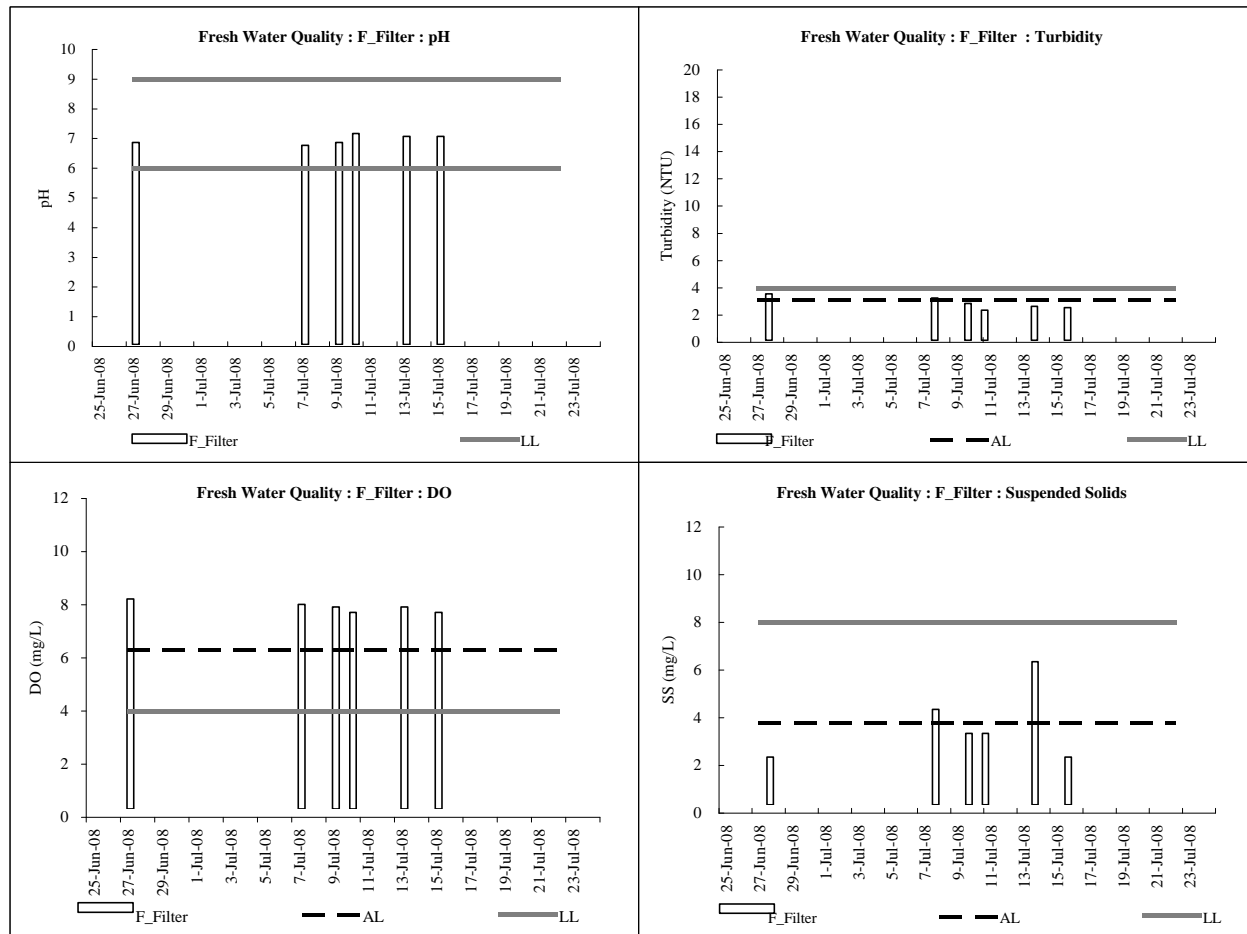


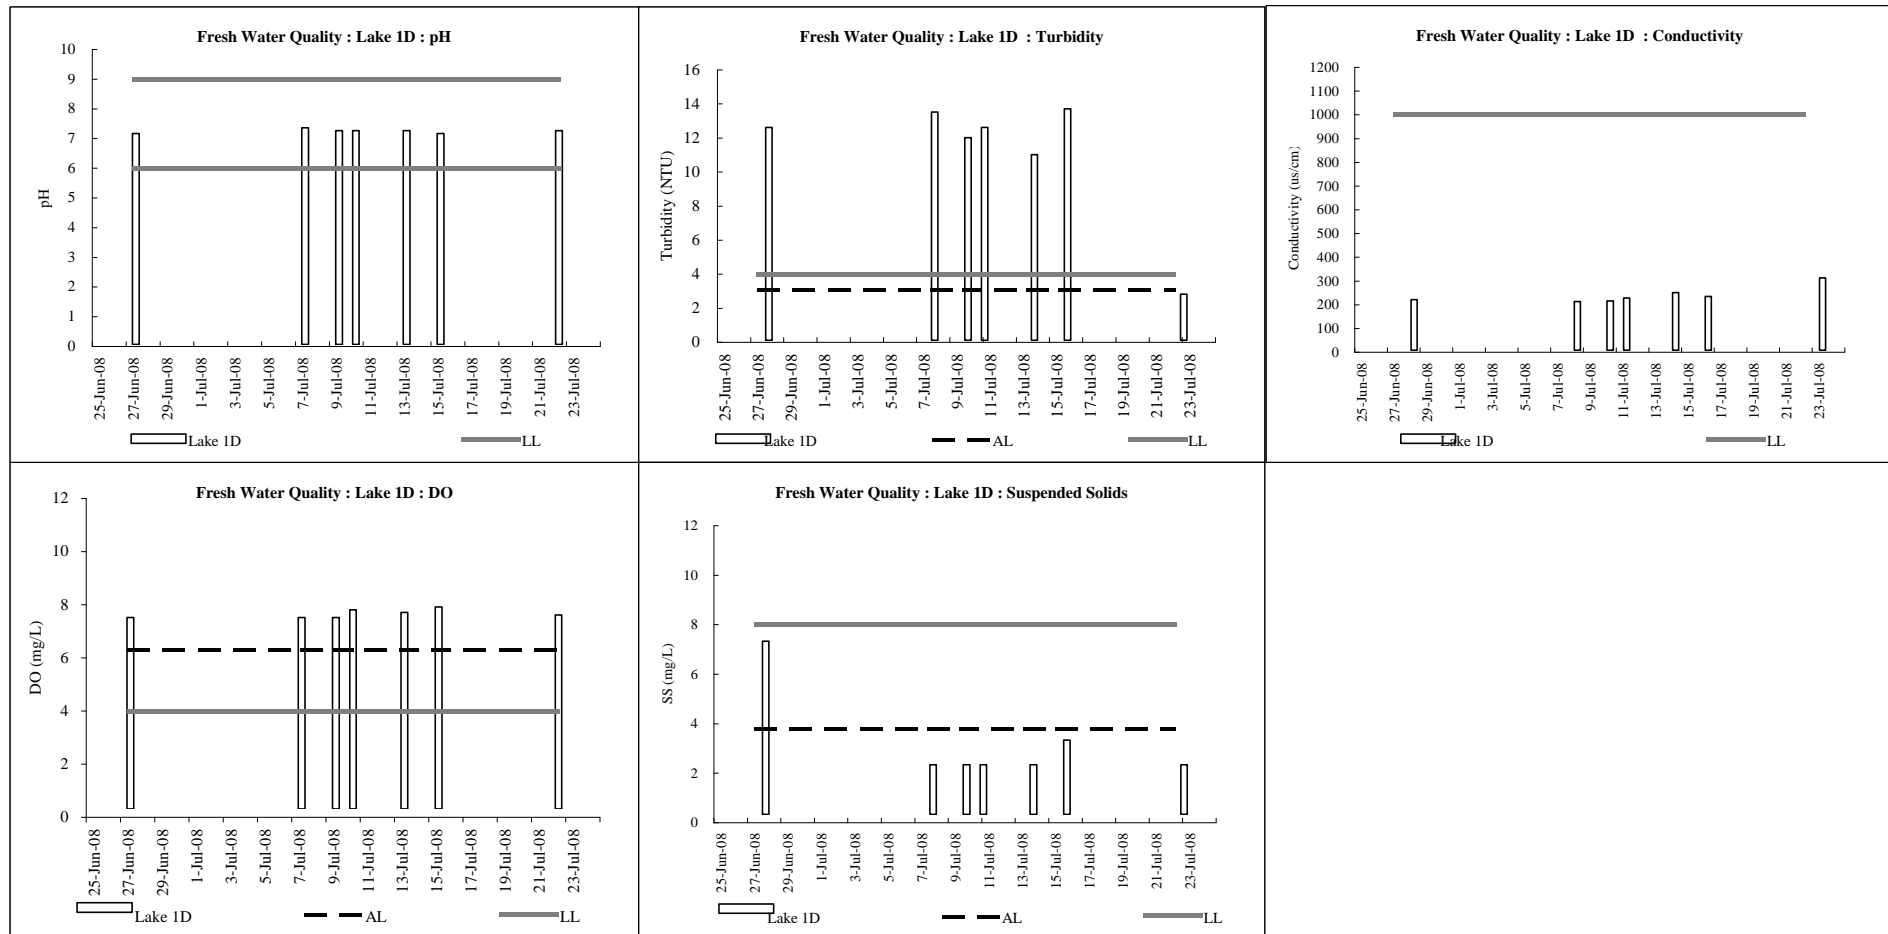


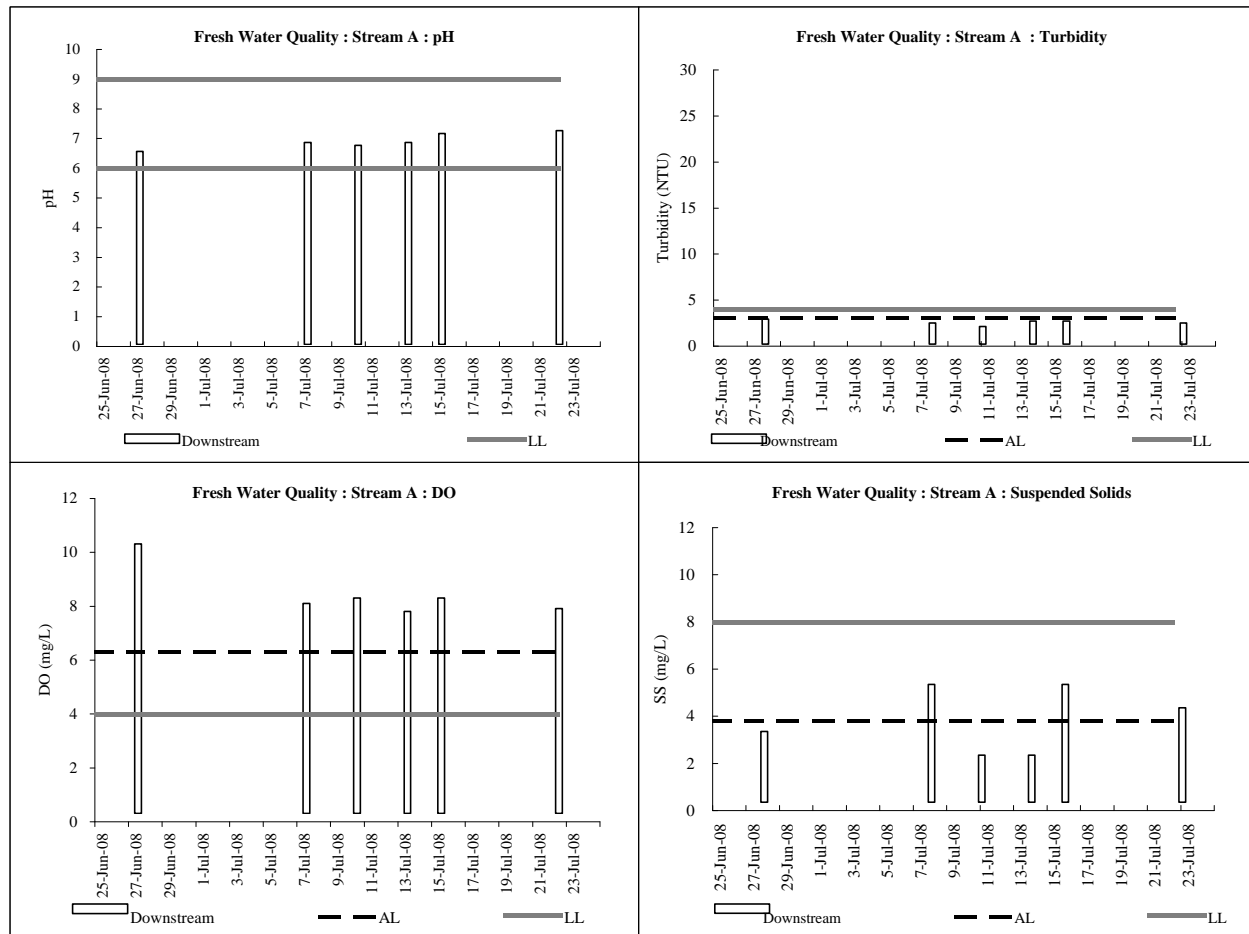







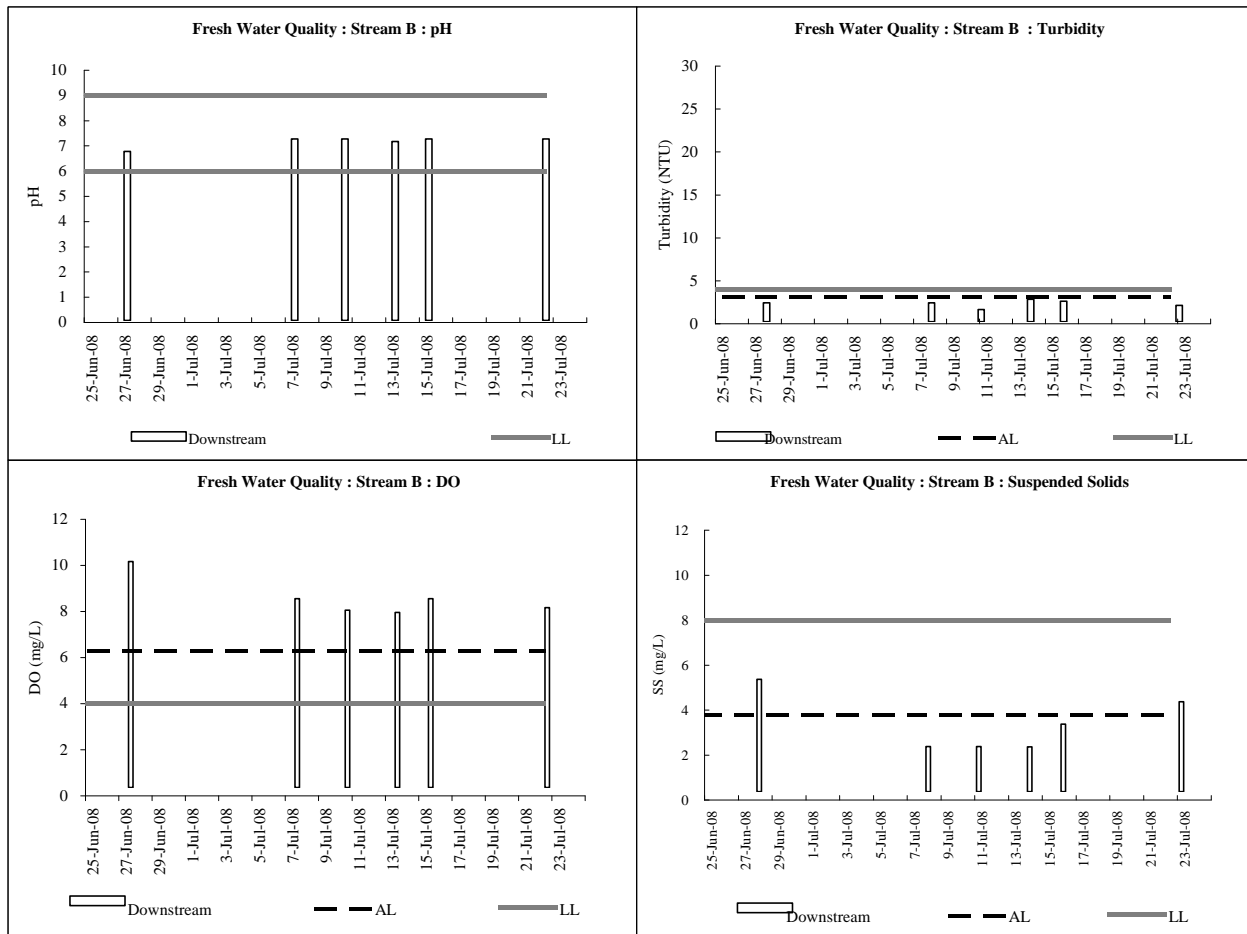





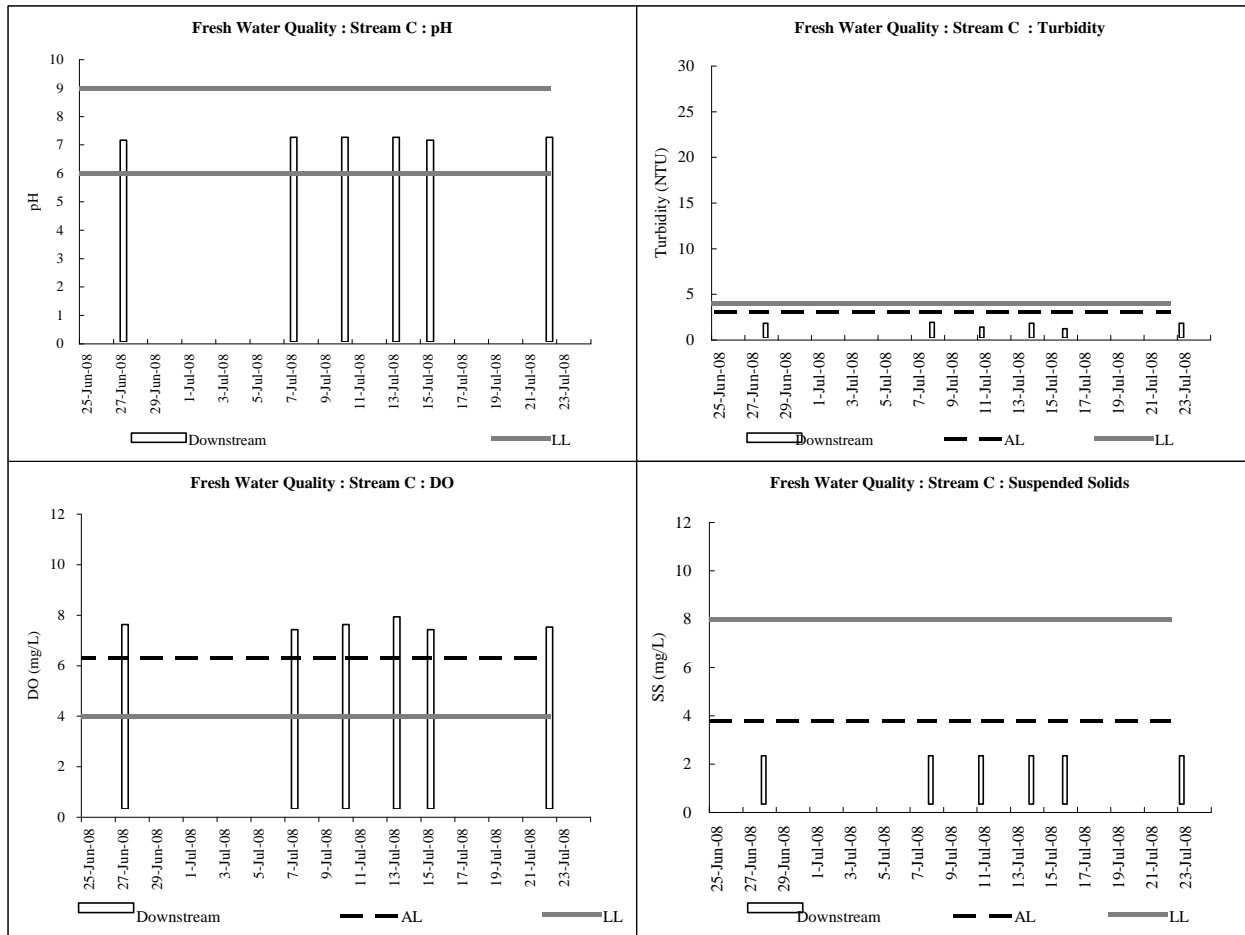


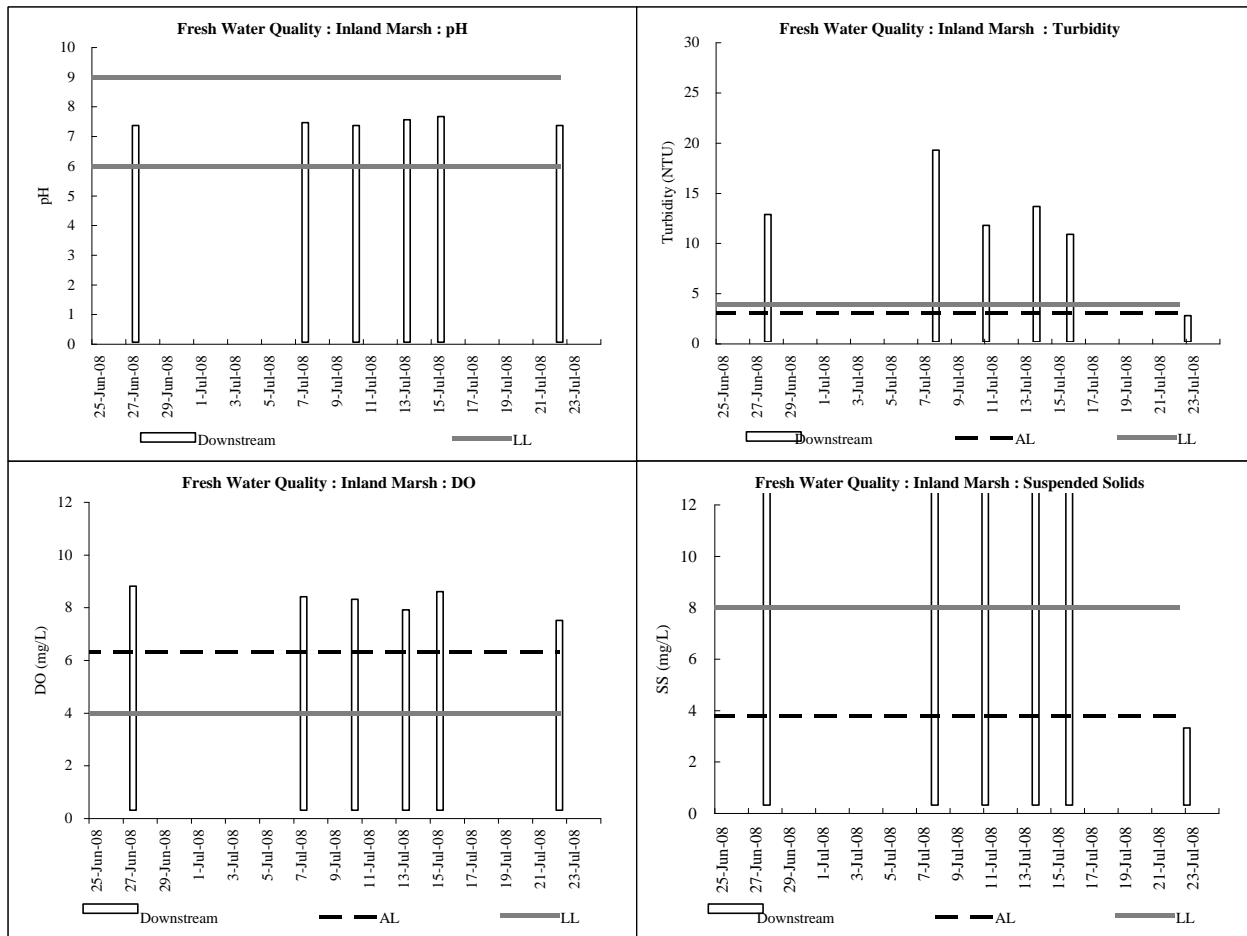


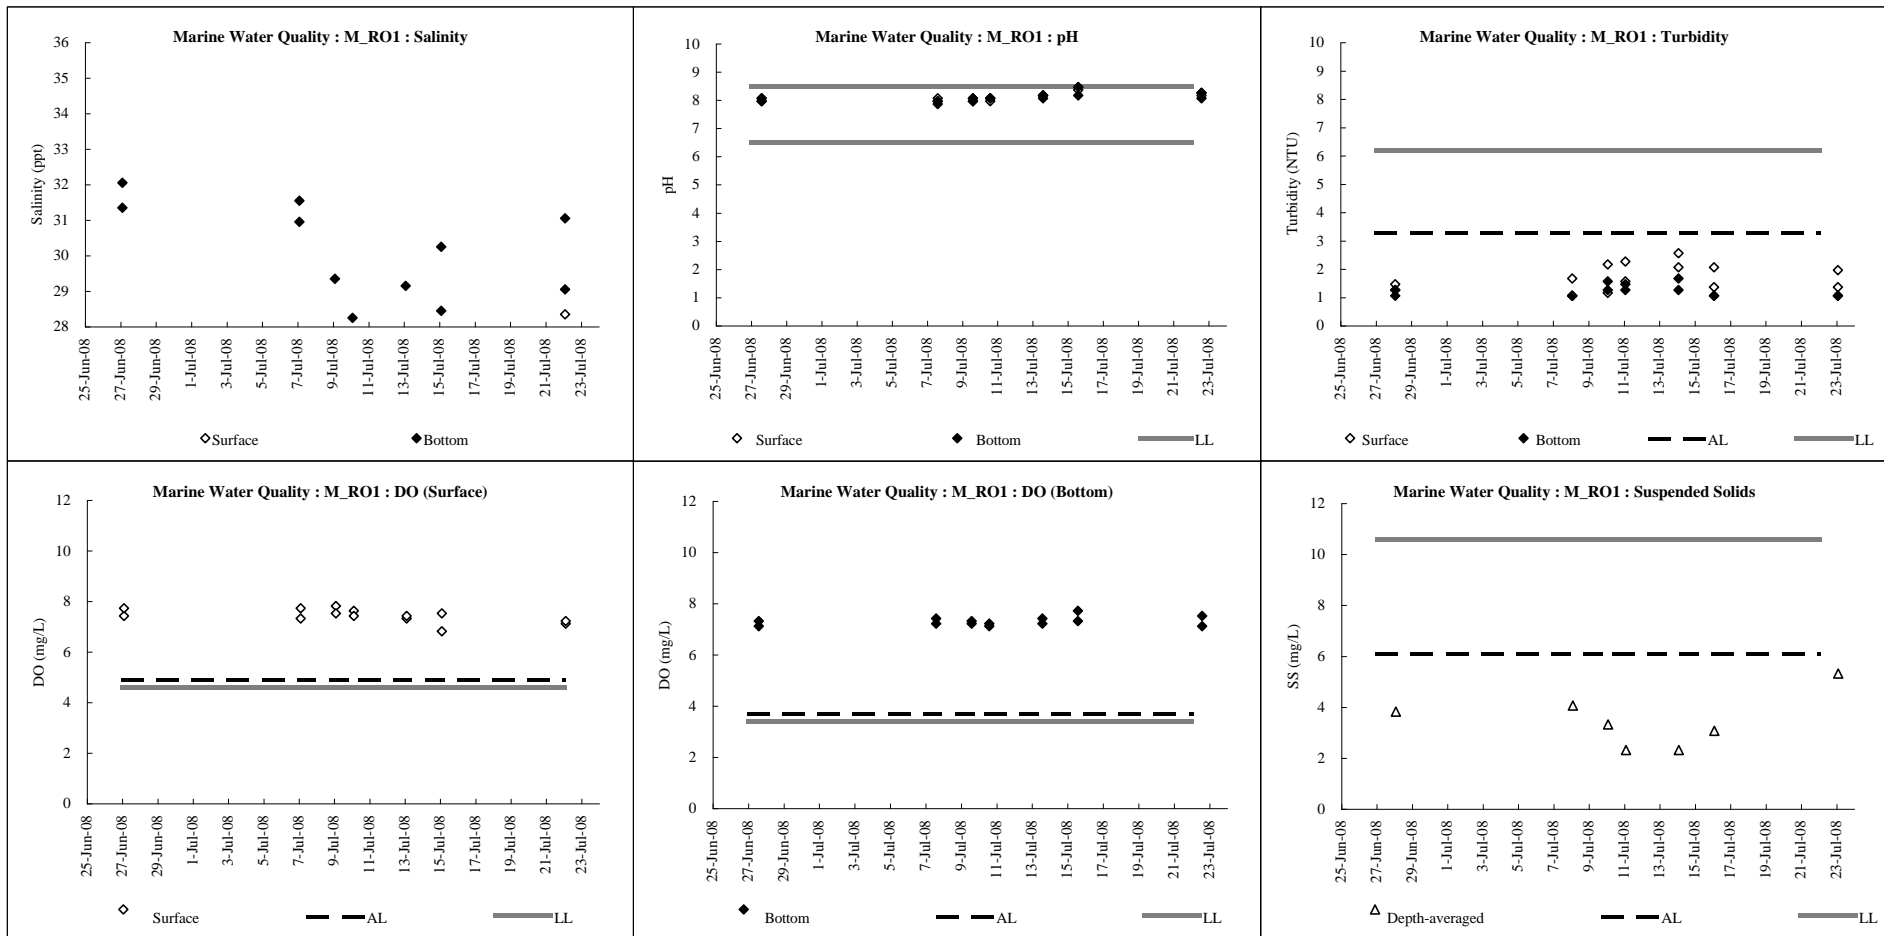


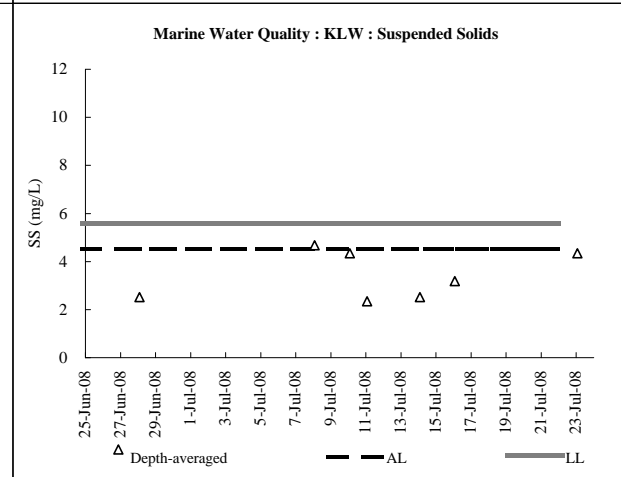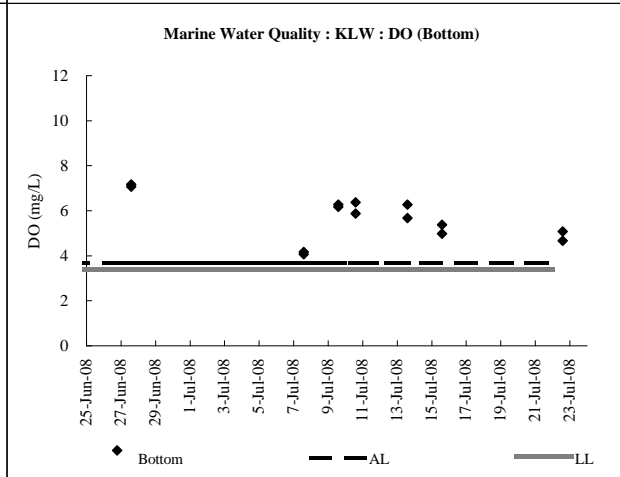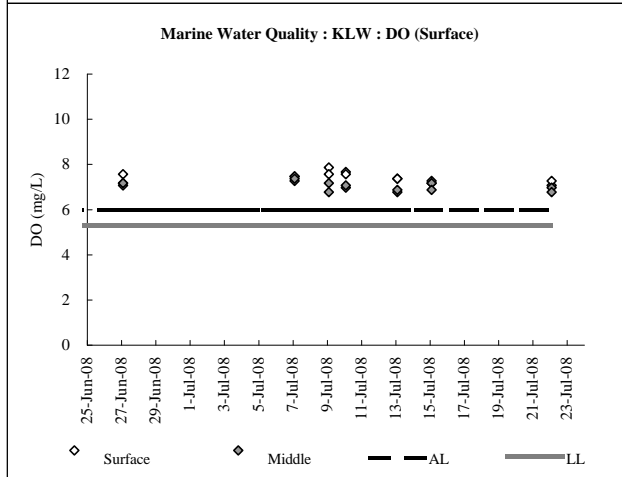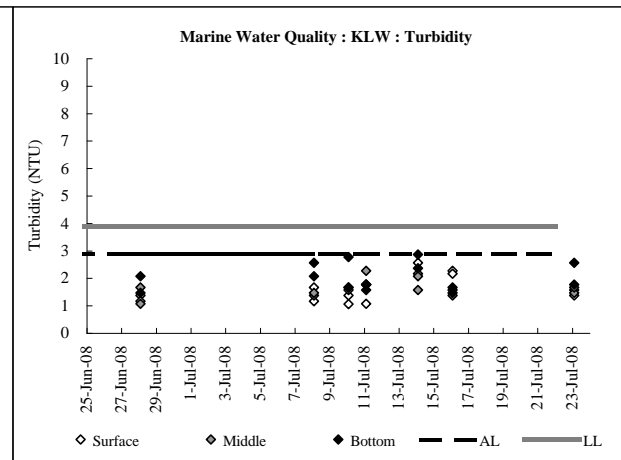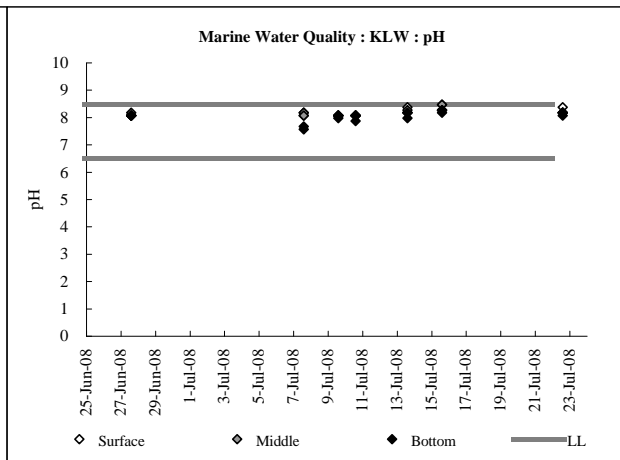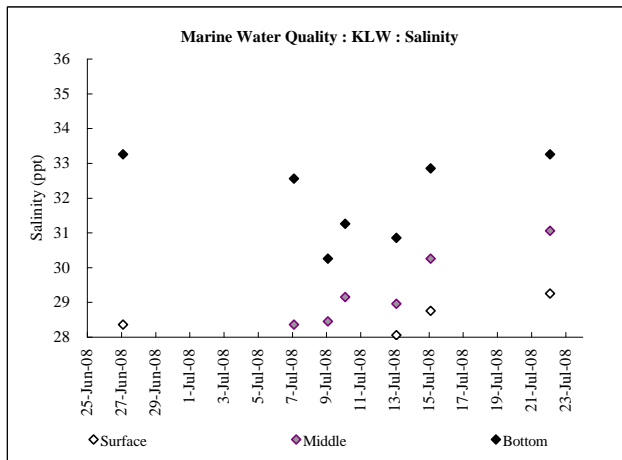

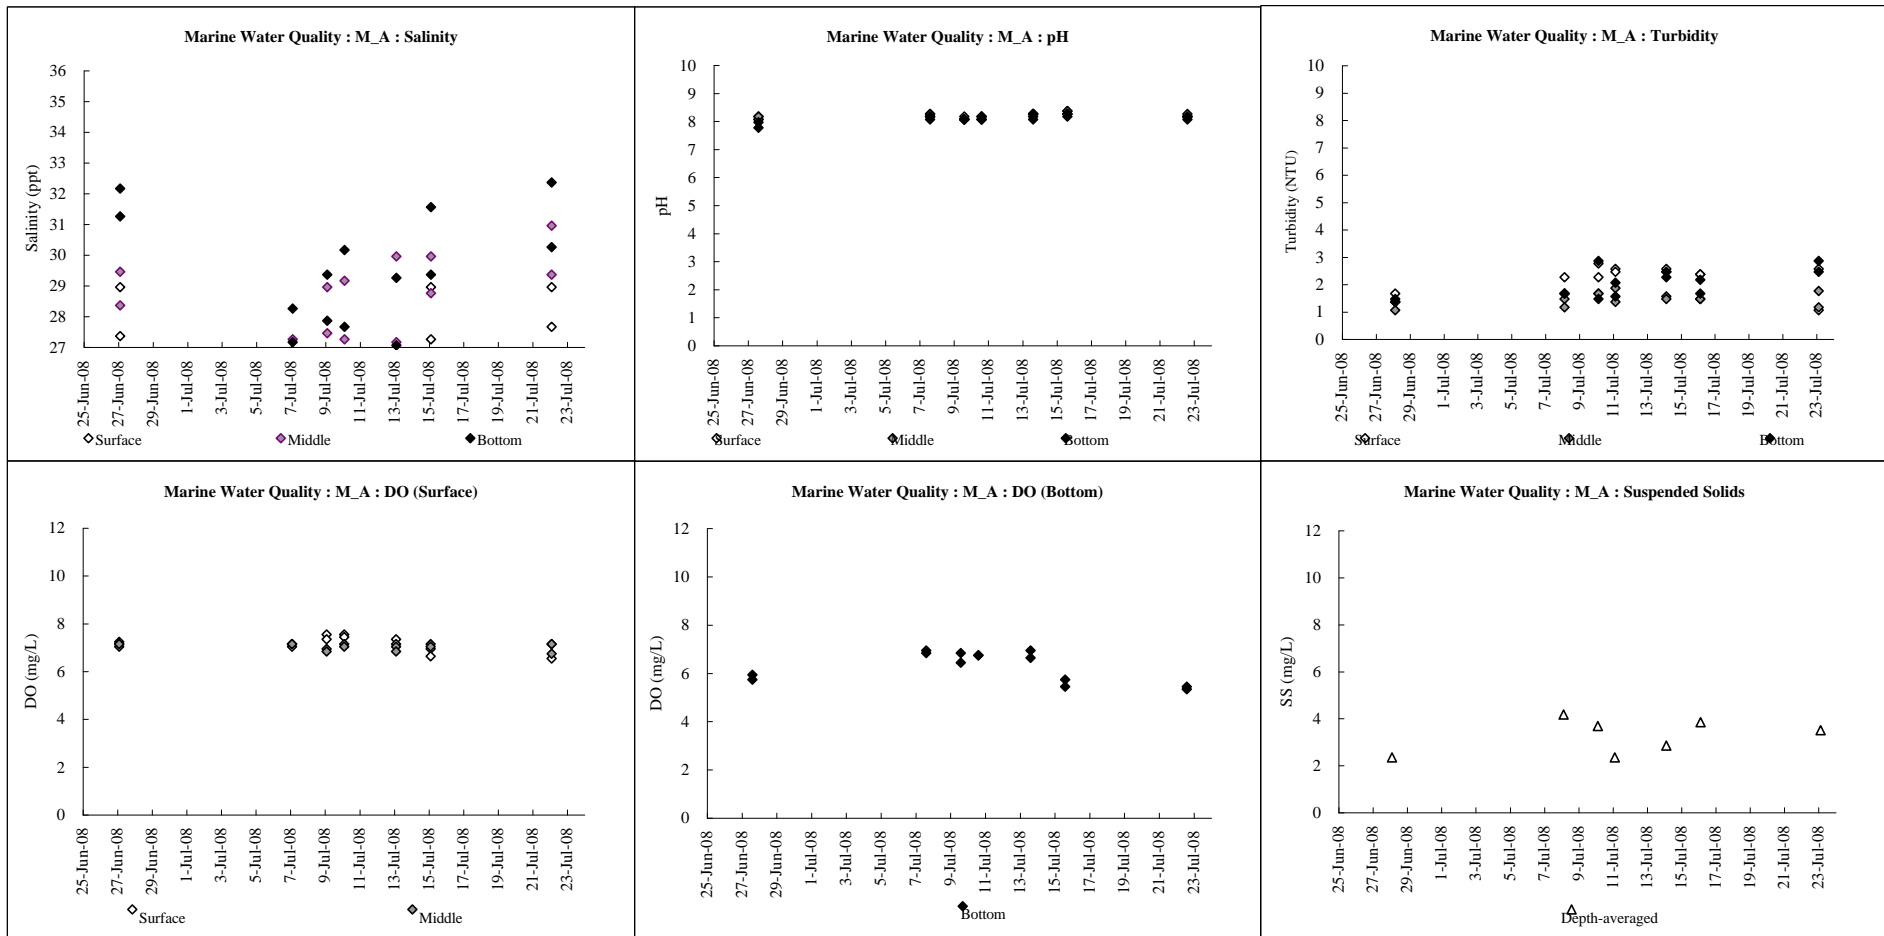


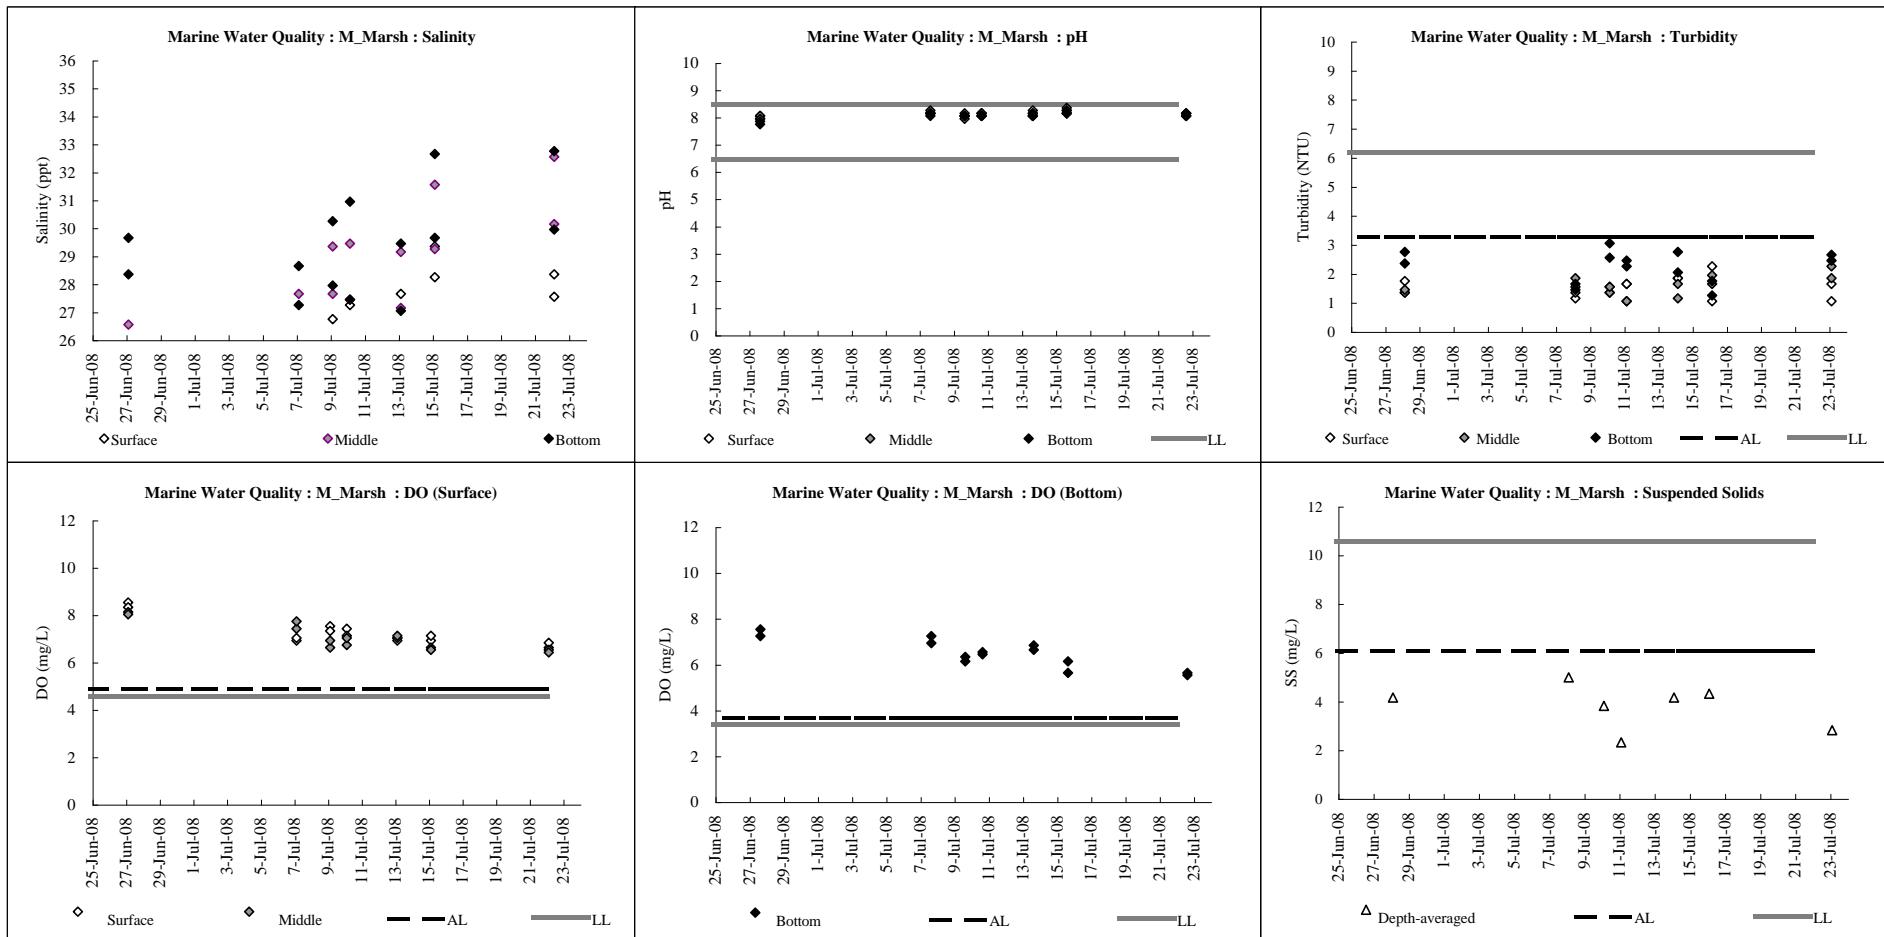


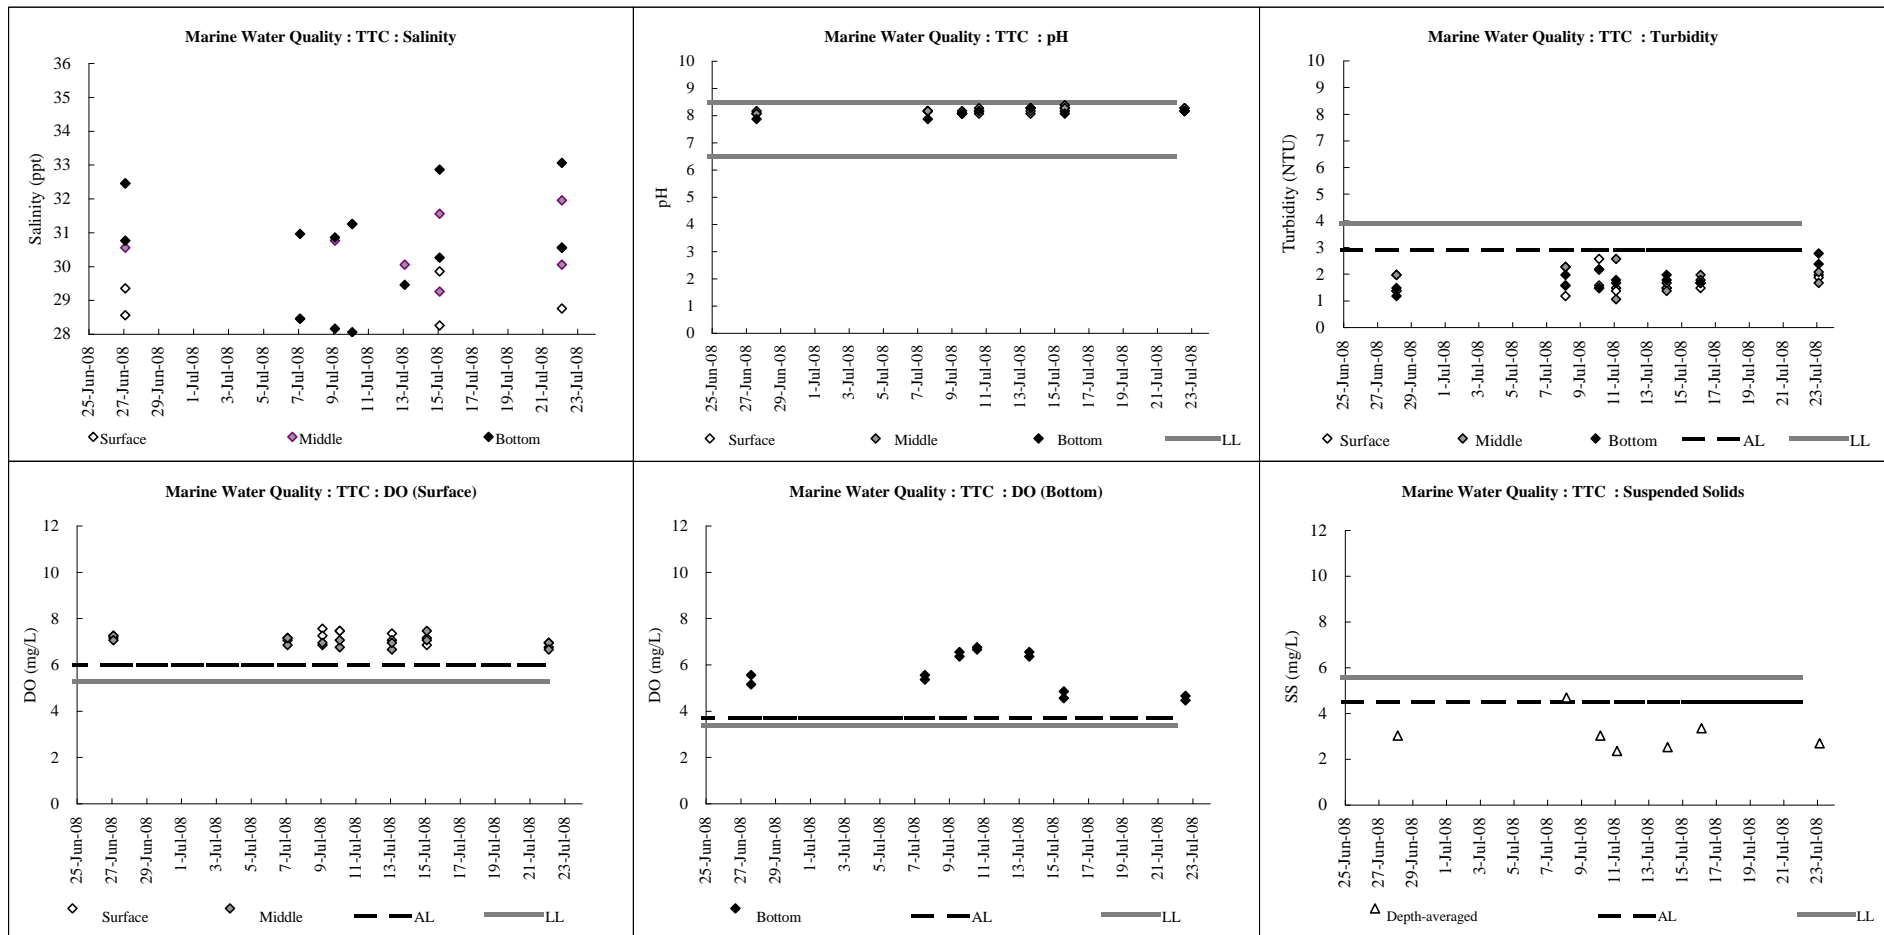

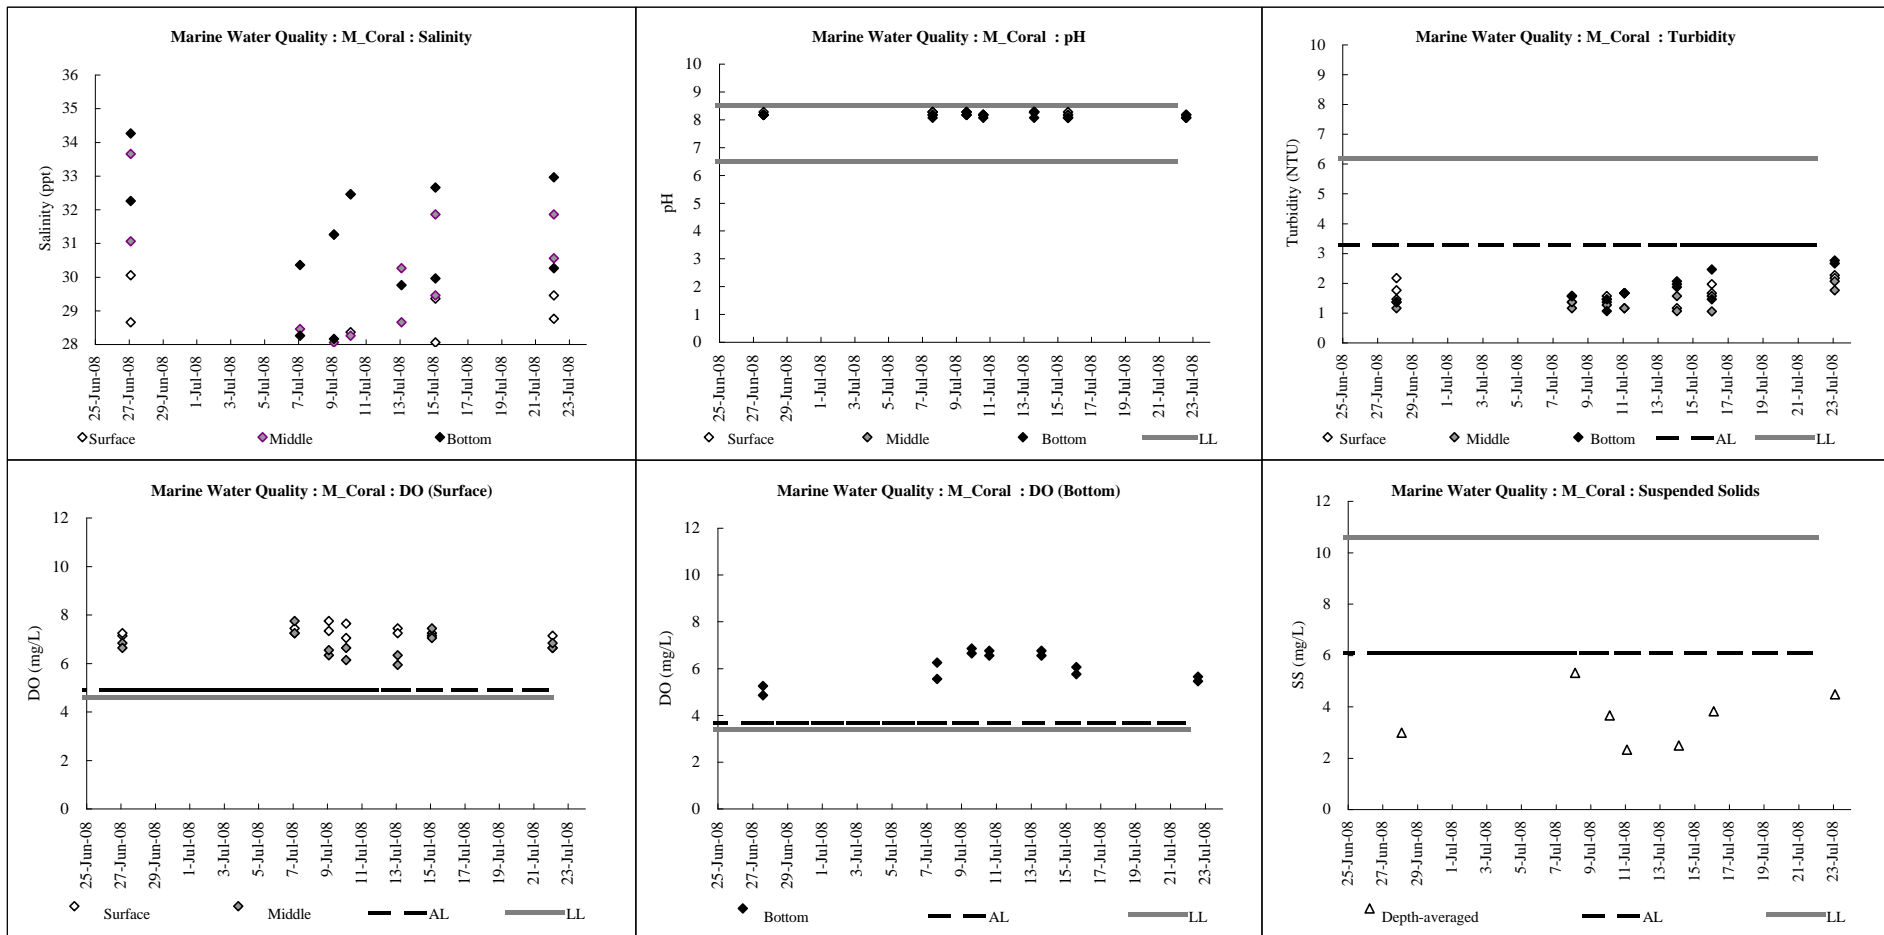



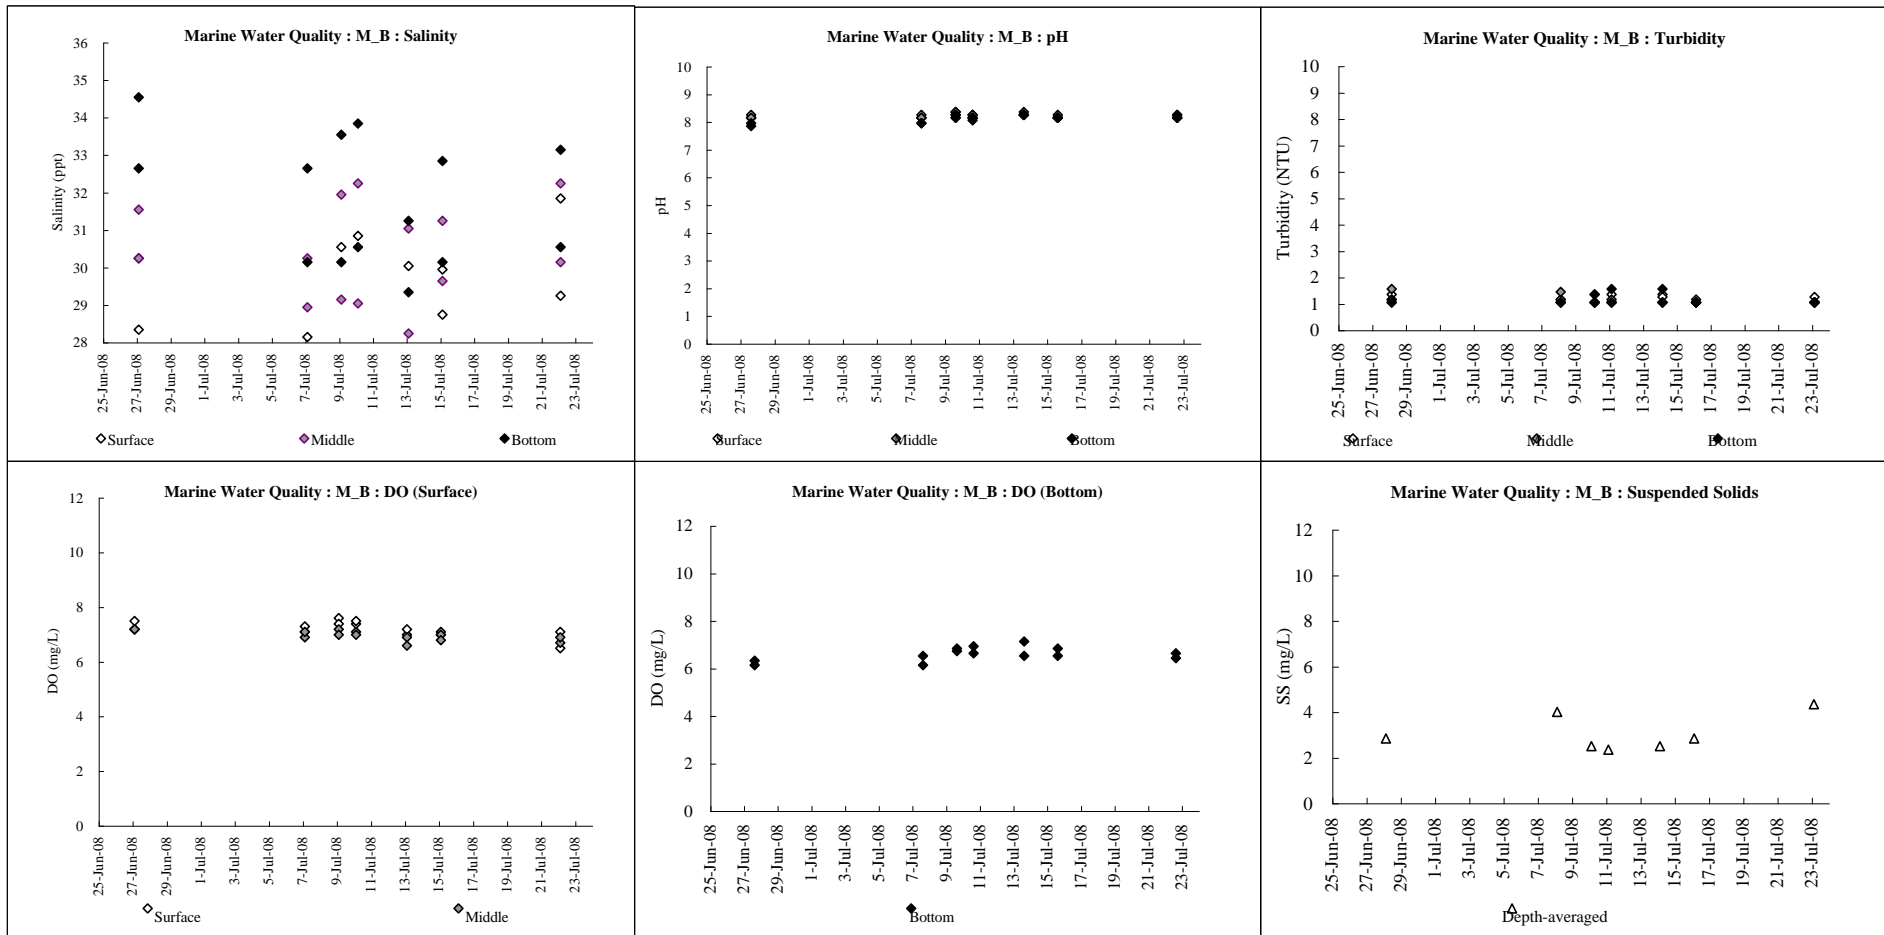

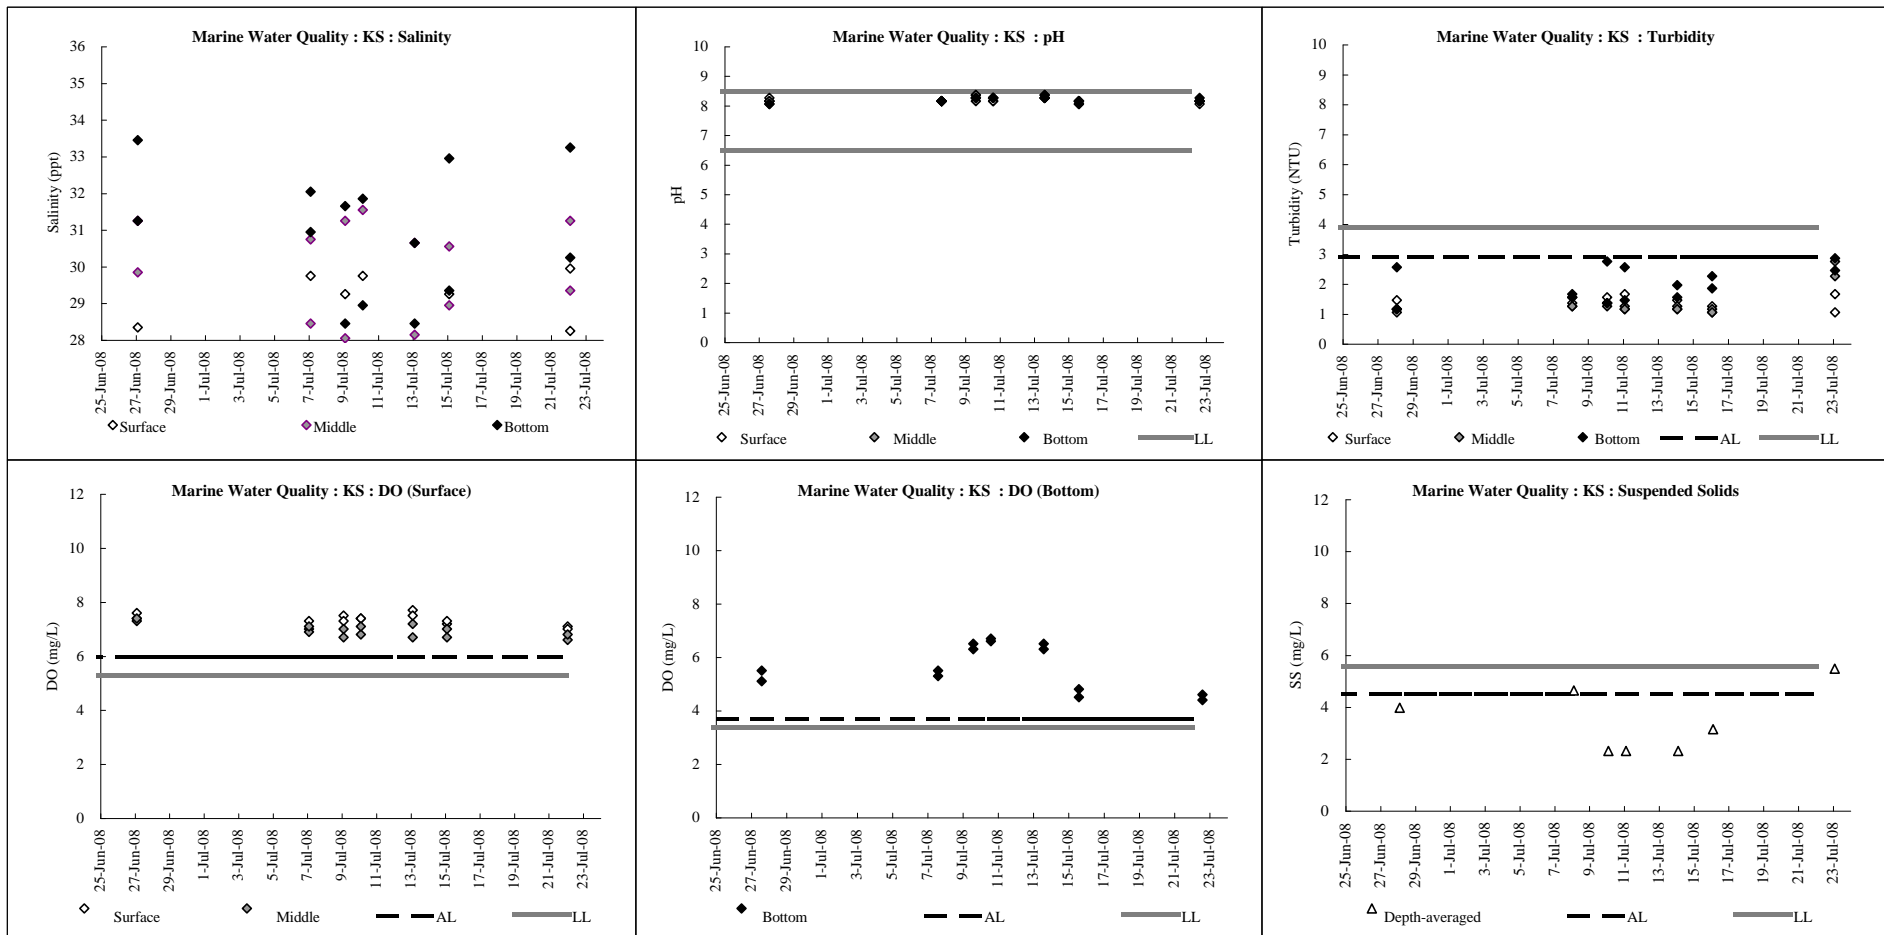

# Marine Ecology

Operation Phase  
Baseline in Jul 08

Previsous Construction  
Phase Conditions in Dec 07

X-01



X-02



X-03



X-04



X-05

Missing

Missing

Operation Phase  
Baseline in Jul 08

Previsous Construction  
Phase Conditions in Dec 07

X-06




X-07



X-08



X-09

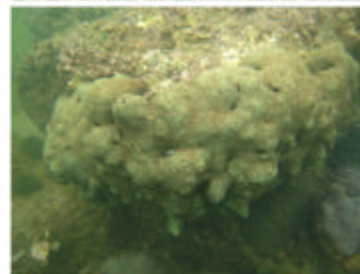

X-10





Operation Phase  
Baseline in Jul 08

Previous Construction  
Phase Conditions in Dec 07

X-11



X-12



X-13



X-14



X-15



Operation Phase  
Baseline in Jul 08

Previous Construction  
Phase Conditions in Dec 07

X-16



X-17



X-18



X-19



X-20








Operation Phase  
Baseline in Jul 08

Previous Construction Phase  
Conditions in Dec 07

Operation Phase  
Baseline in Jul 08

Previous Construction Phase  
Conditions in Dec 07

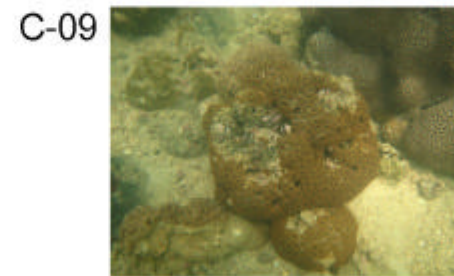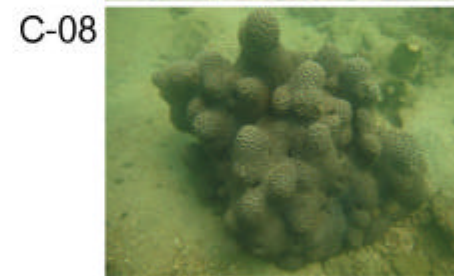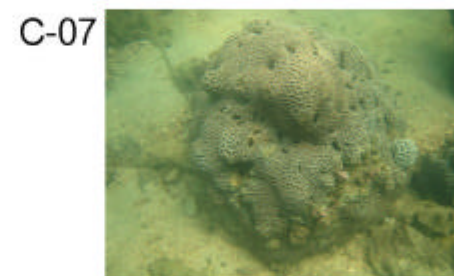



Operation Phase  
Baseline in Jul 07

Previous Construction Phase  
Conditions in Dec 07

C-11



C-12



C-13



C-14



C-15



Operation Phase  
Baseline in Jul 07

Previous Construction Phase  
Conditions in Dec 07

C-16



C-17



C-18



C-19



C-20

Missing





Operation Phase  
Baseline in Jul 08

D-01



D-02



D-03



D-04



D-05



Operation Phase  
Baseline in Jul 08

D-06



D-07




D-08



D-09



D-10

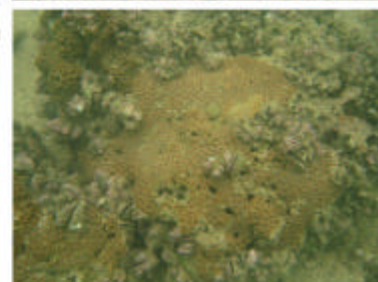



Operation Phase  
Baseline in Jul 08

D-11



D-12



D-13



D-14



D-15



Operation Phase  
Baseline in Jul 08

D-16



D-17



D-18



D-19



D-20



# **Annex D**

## **Calibration Certificates**



Environmental Division

## CERTIFICATE OF ANALYSIS

**CONTACT:** MR WONG SIU HO  
**CLIENT:** ENOVATIVE ENV TECHNOLOGY CO  
**ADDRESS:** RM 3704 SIK MAN HOUSE  
HOMANTIN ESTATE  
KOWLOON  
**ORDER No.:**  
**PROJECT:**

**Batch:** HK116788  
**Sub Batch:** 0  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 25/07/2008  
**DATE OF ISSUE:** 30/07/2008  
**SAMPLE TYPE:** EQUIPMENT  
**No. of SAMPLES:** 1

### COMMENTS

The calibration procedure used for the analysis has been applied for the calibration of the above instrument.

### NOTES


This is the Final Report and supersedes any preliminary report with this batch number.  
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

### ISSUING LABORATORY: HONG KONG

#### Address

ALS Technichem (HK) Pty Ltd  
11/F  
Chung Shun Knitting Centre  
1-3 Wing Yip Street  
Kwai Chung  
HONG KONG

**Phone:** 852-2610 1044  
**Fax:** 852-2610 2021  
**Email:** hongkong@alsenviro.com

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong

#### Other ALS Environmental Laboratories

**AUSTRALIA**  
Brisbane  
Melbourne  
Sydney  
Newcastle

**AMERICAS**  
Vancouver  
Santiago  
Atofagasta  
Lima

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., H.K.

Phone: 852-2610 1044 Fax: 852-2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company

*This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.*

# CERTIFICATE OF ANALYSIS



Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of Tubidimeter

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2130B  
Date of Calibration : 25 July, 2008

### Testing Results :

Expected Reading	Recording Reading
0.00 NTU	0.1 NTU
4.00 NTU	3.94 NTU
16.0 NTU	16.2 NTU
80.0 NTU	80.5 NTU
160 NTU	161 NTU
Allowing Deviation	±10%

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong

# CERTIFICATE OF ANALYSIS



Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of Conductivity System

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2510B  
Date of Calibration : 25 July, 2008

### Testing Results :

Expected Reading	Recording Reading
1412 uS/cm	1416 uS/cm
6667 uS/cm	6670 uS/cm
58670 uS/cm	58610 uS/cm
Allowing Deviation	±10%

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong



# CERTIFICATE OF ANALYSIS



Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of Salinity System

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 2520 A and B  
Date of Calibration : 25 July, 2008

### Testing Results :

Expected Reading	Recording Reading
10.0 g/L	10.1 g/L
20.0 g/L	20.0 g/L
30.0 g/L	30.2 g/L
Allowing Deviation	±10%

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong

# CERTIFICATE OF ANALYSIS




Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of Thermometer

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : In-house Method  
Date of Calibration : 25 July, 2008

### Testing Results :

Reference Temperature (°C)	Recorded Temperature (°C)
3.5 °C 20.7 °C	3.5 °C 20.6 °C
Allowing Deviation	±2.0°C

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong

# CERTIFICATE OF ANALYSIS



Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of DO System

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : This meter was calibrated in accordance with standard method APHA (18th Ed.) 4500-0C & G  
Date of Calibration : 25 July, 2008

### Testing Results :

Expected Reading	Recording Reading
0.00 mg/L	0.10 mg/L
2.41 mg/L	2.39 mg/L
3.98 mg/L	4.01 mg/L
7.94 mg/L	7.89 mg/L
Allowing Deviation	±0.2 mg/L

  
\_\_\_\_\_  
Alice W M Wong  
Laboratory Manager - Hong Kong



# CERTIFICATE OF ANALYSIS



Batch: HK116788  
Sub Batch : 0  
Date of Issue: 30/07/2008  
Client: ENOVATIVE ENV TECHNOLOGY CO  
Client Reference:

## Calibration of pH System

Item : YSI SONDE Environmental Monitoring System  
Model No. : 6920  
Serial No. : 000109DF  
Calibration Method : This meter was calibrated in accordance with standard method APHA (19th Ed.) 4500 H:B  
Date of Calibration : 25 July, 2008

### Testing Results :

Expected Reading	Recording Reading
4.00	4.00
7.00	7.00
10.0	9.99
Allowing Deviation	±0.2 unit

  
Ms Wong Wai Man, Alice  
Laboratory Manager - Hong Kong



# **Annex E**

## **Fertilizer and Pesticides Application**



Remarks:

1. Dosage Application by JCKSC

F (follow with numbers) – fertilizers were applied at those holes of East Golf Course.

C (follow with numbers) – non-biological chemicals (eg. pesticides, fungicides, etc.) were applied at those holes of East Golf Course.

2. Weather Information (from Hong Kong Observatory)



daily duration of sunshine > 4 hours and without raining



daily rainfall > 0.5 mm at Kau Sai Chau Island



daily duration of sunshine < 4 hours and without raining




daily rainfall > 30 mm at Kau Sai Chau Island

{R} Rainstorm signal was hoisted; “A” stands for Amber, “R” stands for Red and “B” stands for Black rainstorm signals were hoisted.

3. Environmental Monitoring

WQ – fresh and marine water quality monitoring were implemented.

# FIGURES

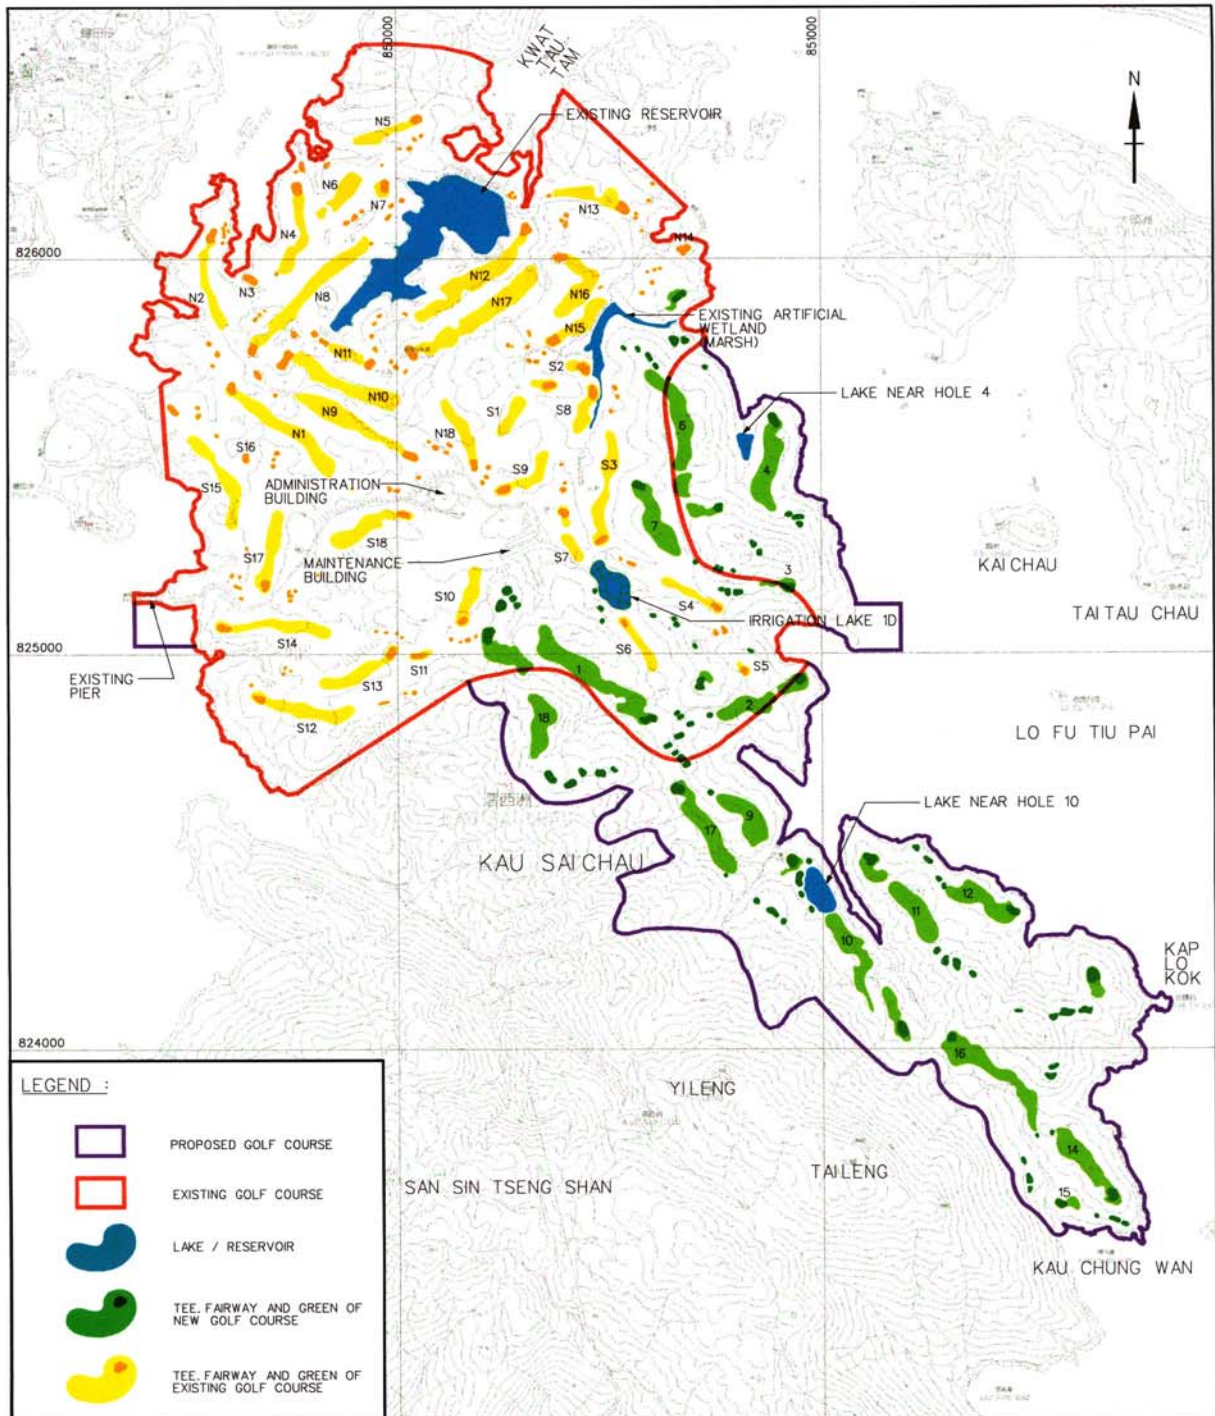


 The Hong Kong Jockey Club

---



  
**BLACK & VEATCH HONG KONG LIMITED**  
 博威工程顧問有限公司

**PROPOSED EXTENSION OF PUBLIC GOLF**  
**Public Golf Course at Kau Sai Chau Island,**  
**Sai Kung**

Master Layer Plan

<b>Fig 1.1</b>	Revision
Reference	File Name
Prepared	Checked
Date	Scale
Apr 08	1: 15000 (A4)



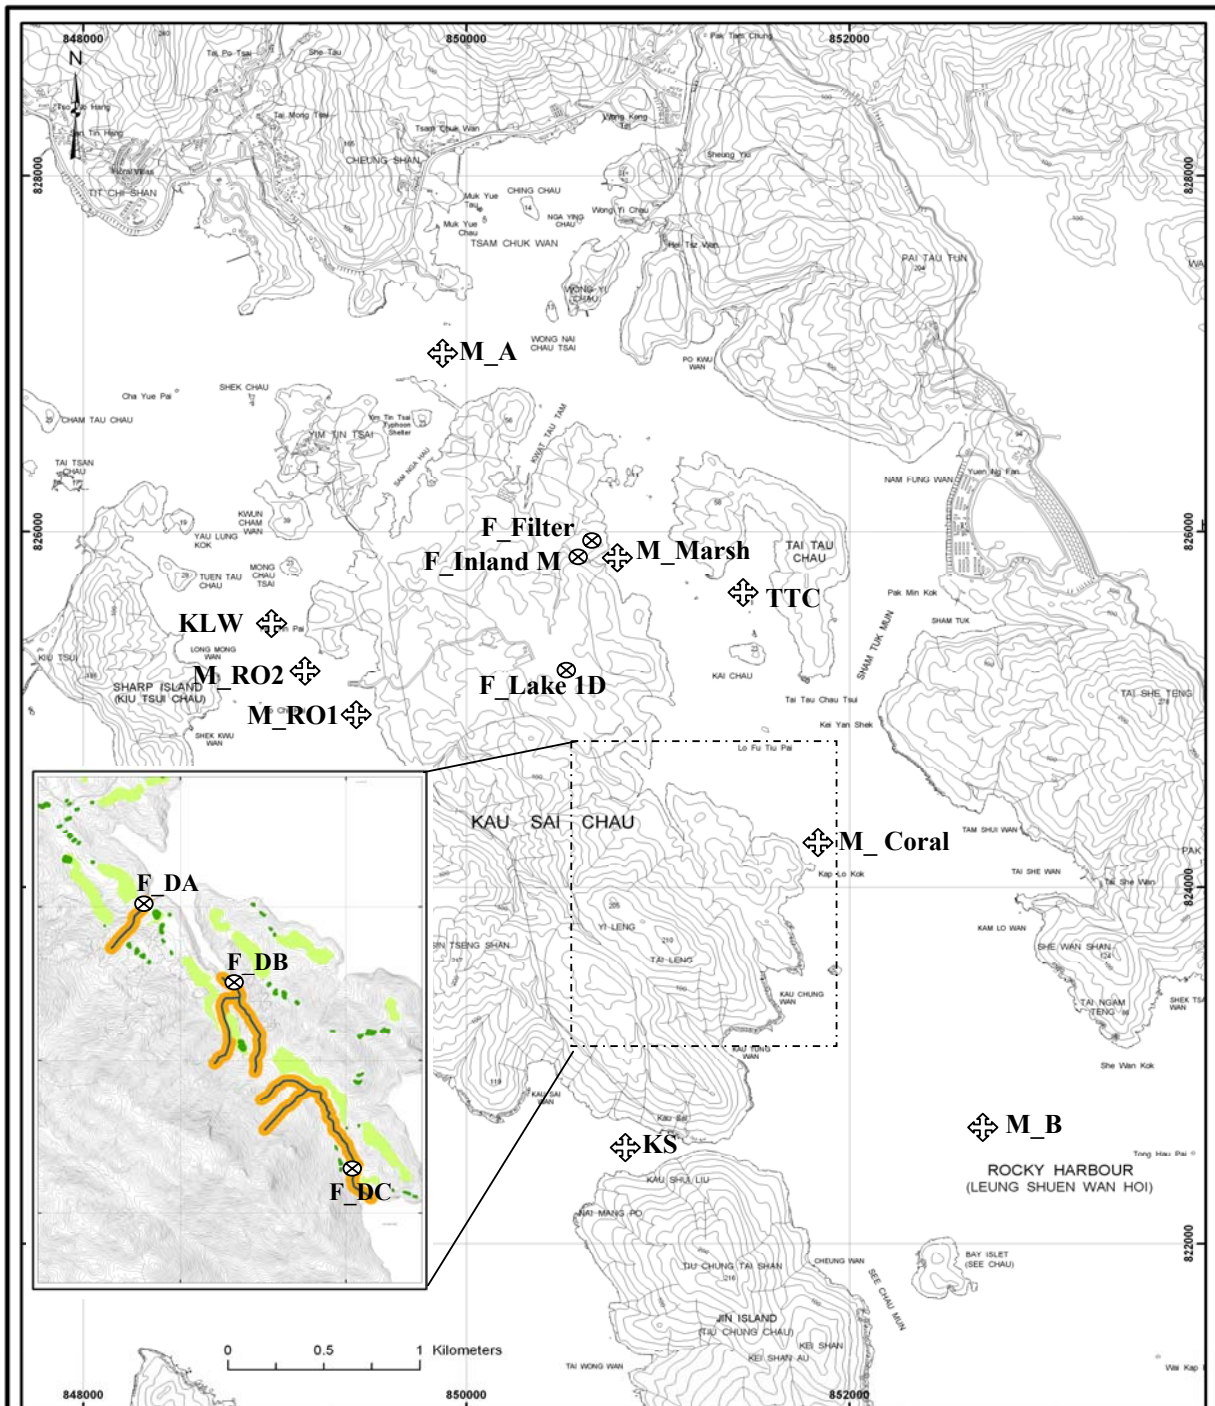


 香港賽馬會  
 The Hong Kong Jockey Club



 BLACK & VEATCH HONG KONG LIMITED  
 博威工程顧問有限公司

Public Golf Course at Kau Sai Chau Island, Sai Kung  
 Water Quality Monitoring Locations -  
 Operation Phase

Fig 3.1	
ET	PKL
Apr 08	

MXD file C:\P566\0\Project\032219\_0222\location.mxd  
 Plot file C:\P566\0\Project\032219\_0222\location.pdf



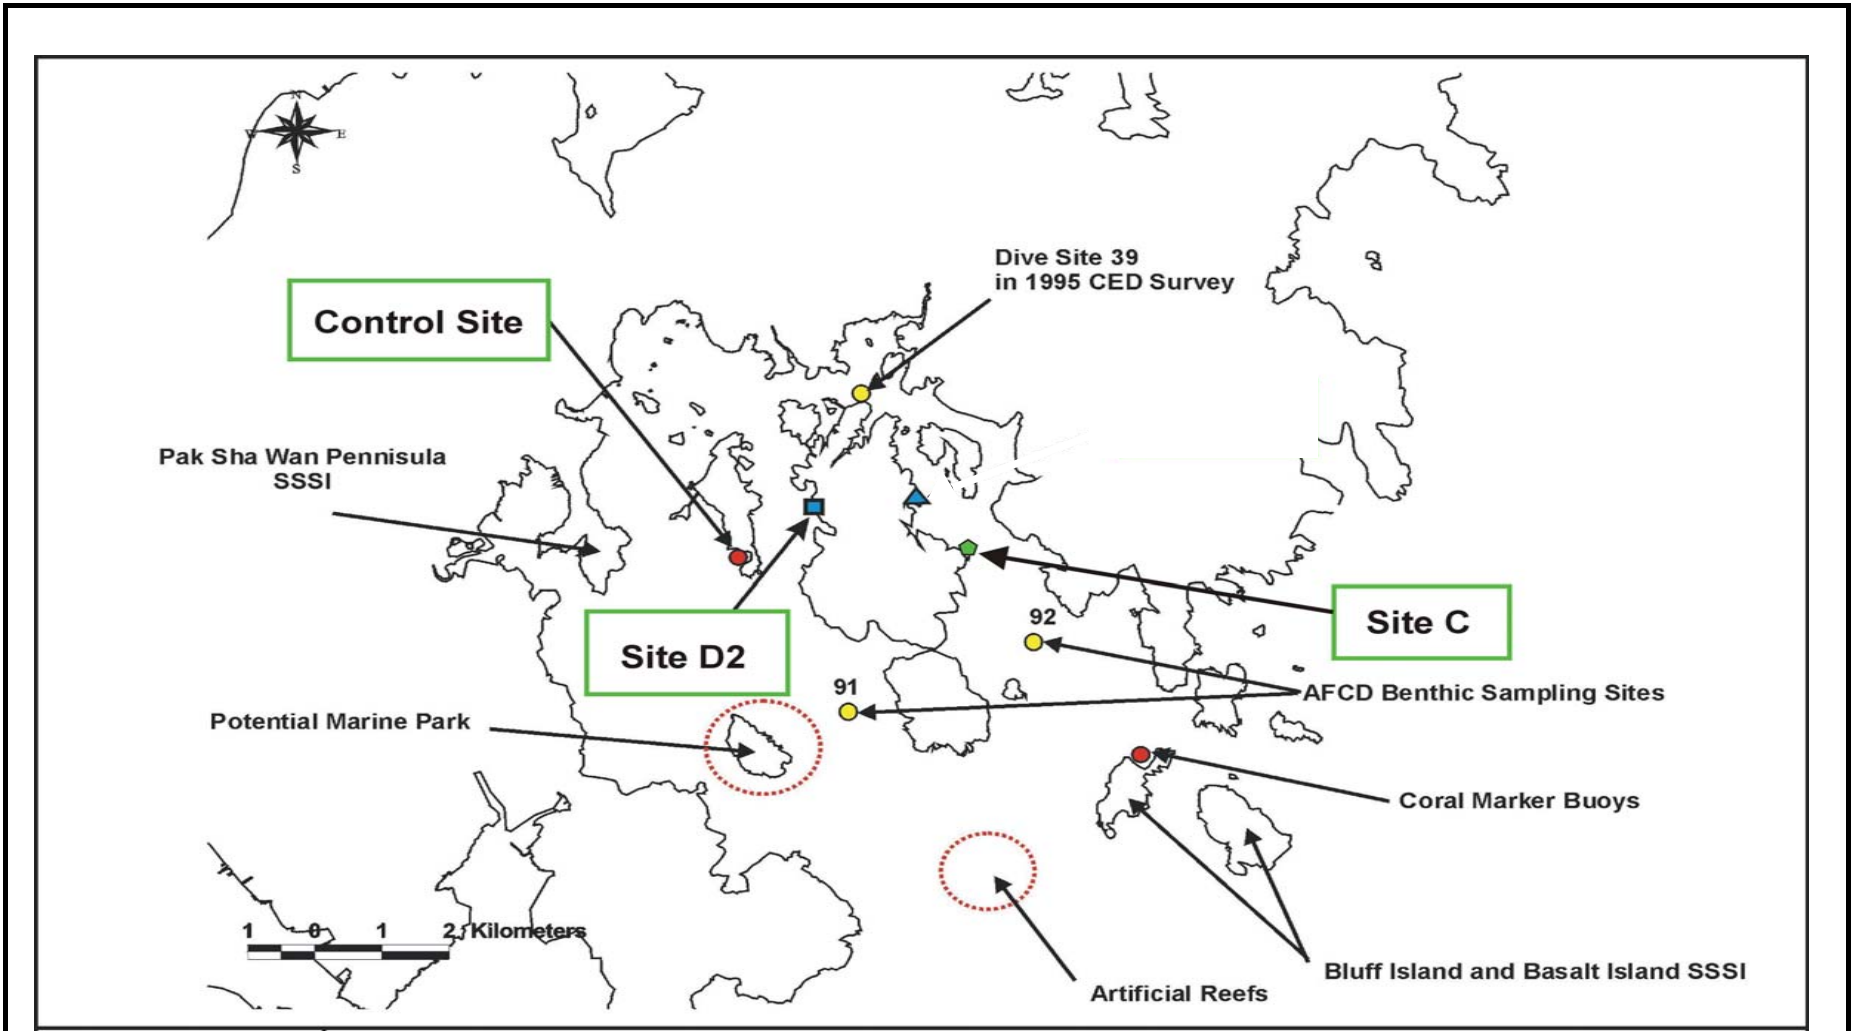

香港賽馬會  
The Hong Kong Jockey Club



BLACK & VEATCH HONG KONG LIMITED  
博威工程顧問有限公司

Proposed Extension of Public Golf Course at Kau Sai Chau Island, Sai Kung

Coral Survey Monitoring Location

Fig 3.2

Prepared	Checked
ET	PKL
Date	Apr-08
