


Ocean Park Master Redevelopment Project

EP-249/2006/A – Condition 3.4

Monthly EM&A Report – July 2011

Certified by  on 18-Aug-11
Lindsay Pickles (ETL)

Verified by Independent Environmental Checker on 29-August-11
IEC Certificate attached in the submission? Yes

Ocean Park Master Redevelopment Project

Environmental Permit No. EP-249/2006/B - Condition 3.4

Monthly EM&A Report – July 2011

Submitted by Ocean Park Corporation on 18-08-2011

This is to verify that

Monthly EM&A Report – July 2011

Submitted by Ocean Park Corporation

On 18-08-2011

Has been verified by the undersigned.

Signed



Dr Anne F Kerr
Independent Environmental Checker (IEC)
Retained by Ocean Park Corporation
pursuant to Environmental Permit No. EP-249/2006/B

Date

29 August 2011



Ocean Park Master Redevelopment Project

Monthly Environmental Monitoring & Audit Report – July 2011



Table of Content

Part 1 Project Overview

Executive Summary

1.	Introduction.....	3
2.	Project Organisation	4
3.	Construction Works Undertaken during the Reporting Month	4
4.	Permits and License Status	5
4.1	ENVIRONMENTAL PERMIT.....	5
4.2	CNP	5
4.3	OTHER PERMITS & LICENSES	6
5.	EP Submissions Status.....	6
6.	Materials Management	7
7.	Environmental Monitoring and Results.....	7
7.1	MONITORING REQUIREMENTS	7
7.1.1	CONSTRUCTION MONITORING	7
7.2	MONITORING RESULTS	9
7.2.1	CONSTRUCTION MONITORING RESULTS.....	9
7.2.2	OPERATIONAL STAGE MONITORING FOR OCEAN PARK SYMBIO SHOW	10
8.	Site Audit	11
8.1	IEC SITE AUDIT	11
8.2	NON- COMPLIANCE.....	12
9.	Implementation status of Environmental Mitigation Measures.....	12
10.	Summary of Complaint, Summon or Prosecution	12
11.	Future Issues.....	12
12.	Conclusion and Recommendation.....	13
12.1	CONCLUSION	13
12.2	RECOMMENDATION	13

Appendix A IEC's Site Inspection Records

Part 2 CS-03 EM&A Monthly Report

Part 3 Ocean Park Symbio Show 5th Monthly Monitoring Report

Part 1 Project Overview

Executive Summary

This is the combined monthly EM&A Report for Ocean Park Master Redevelopment Project, which includes CS03 "Thrill Mountain and Polar Adventure" under Part 2. This report presents the results of EM&A works conducted in the reporting month of July 2011 (from 26 June 2011 to 25 July 2011) for construction works and in the reporting month of June (27 May 2011 to 26 June 2011) for Operational Monitoring.

Construction works at the Entry Plaza, Aqua City and Grand Aquarium under CI07 have been completed in January 2011 and, as advised to EPD on 1 April (PD/PW/GOV/151/006107), no further construction monitoring will be undertaken.

Construction works at the Summit, CS02 for the Rainforest have been completed in April 2011.

At the Summit, Contract CS03, for the Thrill Mountain and Polar Adventure, is still underway. Other than ongoing Coral Survey, there will be no construction monitoring undertaken. The audits will continue to be carried out by the Contractors ET and OPC's ET and verified by the IEC.

Environmental monitoring for the Park's Operations has commenced upon the opening of Aqua City and with the commencement of the Symbio Show on 27 January 2011. The 5th Air Quality and Noise Monitoring Report for the Ocean Park Symbio Show is included in this report under Part 3.

No complaint, non-compliance from IEC, summons or prosecution related to environmental issues was made against the Ocean Park Master Redevelopment Project in the reporting period of July 2011.

1. Introduction

The "Master Redevelopment Project of Ocean Park" (hereinafter known as the "Project") is implemented by the Ocean Park Corporation at its existing site of Ocean Park and Nam Long Shan, Aberdeen. The Project involves both reconstruction/modification of existing facilities and expansion of the Park under Environmental Permit, EP-249/2006/B.

The construction works of the project consists of various contracts. Details of the contracts, which are required to perform the EM&A programme, are shown below.

Contract No.	Contract Title	Contractor	Construction Commencement
CI-05	Site Formation, Funicular Tunnel and Miscellaneous Works	Dragages-Bouygues JV	12 March 2007 and Construction phase has ceased in early June 2009
CS-01	Back of House for Marine Mammal Veterinary Hospital	Kaden – ATAL JV	26 March 2007 and Construction phase has ceased in mid-October 2008
CW-02	Astounding Asia	W. Hing Construction Co. Ltd.	1 August 2007 and Construction phase has ceased in mid-February 2010
CI-07	Entry Plaza, Aqua City and Grand Aquarium	Leighton Contractors (Asia) Ltd.	15 August 2008 and Construction Phase has ceased in January 2011
CS-02	Rainforest	W. Hing Construction Co. Ltd.	11 May 2009 and construction has ceased in April 2011
CS-03	Thrill Mountain and Polar Adventure	Kaden – ATAL JV	2 November 2009


The Contractors conduct environmental audits during the construction stage and produce contract specific monthly EM&A reports. This is the combined monthly EM&A Report including the IEC audit findings, CS03 Monthly EM&A Report, and the Operational Monitoring Report for the Ocean Park Symbio Show.

This report presents the results of EM&A works conducted in the reporting month of July 2011 (from 26 June 2011 to 25 July 2011) for construction works and in the reporting month of June (27 May 2011 to 26 June 2011) for Operational Monitoring.

2. Project Organisation

The structure of the environmental management team is shown in below figure.

Figure 1.1 – Management Organisation

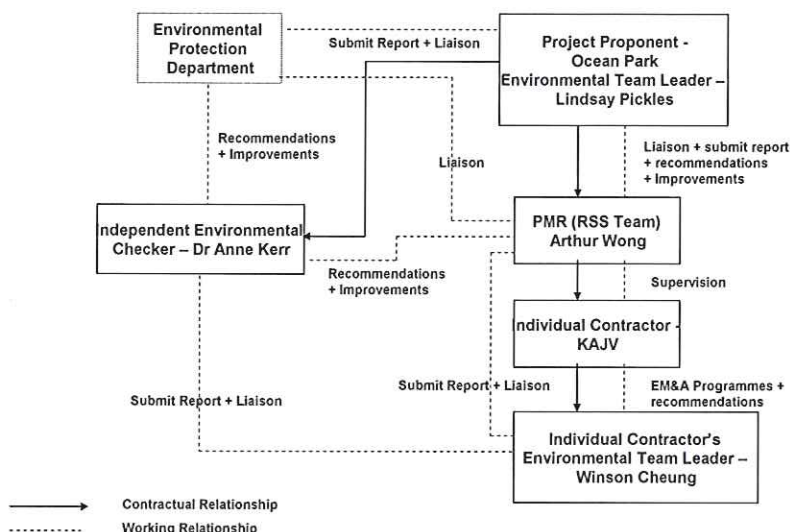

3. Construction Works Undertaken during the Reporting Month

In the reporting month, the construction activities are summarised as follows.

CI-05

- Construction phase has ceased in early June 2009.

CS-01

- Construction phase has ceased in mid-October 2008.

CW-02

- Construction phase has ceased in mid-February 2010.

CI-07

- Construction phase has ceased in January 2011.

CS-02

- Construction phase has ceased in April 2011.

CS-03

- Construction of Tuxedos Restaurant at South Pole;
- Apply waterproofing membrane and carry out water test for roof at North Pole;
- Construction of Bobsled Station superstructure and installation of rides;
- Erection of structure steel works for Thrill Mountain;
- Carry out wall finishing works for PA Building;
- Apply waterproofing at roof of PA Building;
- Trial run of Floorless Coaster;
- Wet trade work at Floorless Coaster;
- Installation of theme works and
- Disposal Existing Stockpile.

4. Permits and License Status

4.1 Environmental Permit

The Environmental Impact Assessment (EIA) Report of the Project has been approved by the Environmental Protection Department (EPD) (Register No.: AEIAR-101/2006) on 12 July 2006. Subsequently, EPD issued Environmental Permit (EP) for the construction and operation of the project. Table below is a full list of the EPs.

EP No.	Issue Date	Key Variation
EP-249/2006	28 July 2006	First EP
EP-249/2006/A	25 September 2006	<ul style="list-style-type: none"> Enhance the roosting habitat for freshwater birds by enlarging Pond 35 and its surrounds with a total area of no less than 120 squares meters and no construction works and discharge from construction sites shall be allowed within Pond 35 after enhancement. Filling of Pond 37 at the Lowland Area. Submission of the as-built drawings showing the enhancement works of Pond 35.
EP-249/2006B	3 November 2010	<ul style="list-style-type: none"> Total sound power level of all loudspeaker clusters shall not exceed 109 db(A) and the sound pressure level at 9m away from each loudspeaker cluster shall not exceed 75 db(A). Submit noise review study. Submit detail design of night time functional and thematic lighting. Trial pyrotechnical special effects materials display and submit air quality sampling plan.

4.2 CNP

Table below shows a list of CNP within the reporting month.

Permit No.	Starting Date	Expired Date	Validity	Location	Contract No.	Status
CS-03 (KAJV)						
GW-RS0036-11	1-Feb-11	31-Jul-11	Various	Top of Nam Long Shan Road	CS03	Valid
GW-RS0516-11	9-June-11	30-Nov-11	Various	Top of Nam Long Shan Road	CS03	Valid

4.3 Other Permits & Licenses

Tables below show lists of other permits & license for individual contracts.

CS-03

Permit/Ref/No	Valid Period		Section	Status
Notification of Construction Work under APCO				
311433	N/A	N/A	Thrill Mountain and Polar Adventure	Valid
Water Discharge License				
WT00005926-2010	12-Feb-10	28-Feb-15	Thrill Mountain and Polar Adventure	Valid
Registration as Chemical Waste Producer				
WPN5213-176-K2880-02	25-Nov-09	N/A	Thrill Mountain and Polar Adventure	Registered
Construction Waste Disposal Billing Account with EPD				
7009695	N/A	N/A	Thrill Mountain and Polar Adventure	Issued

5. EP Submissions Status

Environmental submissions to EPD since the commencement of construction works at Ocean Park, i.e. from 12 March 2007 to 25 July 2011 are as below.

Contract	Submissions
CI-05	<ul style="list-style-type: none"> Notification of Commencement Date Management Organisation Chart Construction Programme Drainage Proposal Silt Curtain Proposal Waste Management Plan Baseline Air Quality and Noise Monitoring Report Transplantation Proposal for Uncommon Species Baseline Coral Survey Report As-built Drawings of Pond 35 Detailed Compensatory Planting As-built Drawing
CS03	<ul style="list-style-type: none"> Monthly EM&A Report (June 2011)
City Bus Limited	<ul style="list-style-type: none"> Written Notice on Completion of TPH Contaminated Soil Disposal Written Notice on Completion of Solidification Treatment of Heavy Metals Contaminated As-built Remediation Plan
Hong Kong School of Motoring Ltd.	<ul style="list-style-type: none"> Confirmation Letter to confirm that Land Contamination remediation Works within HKSM has been completed
Environmental Permit Conditions	<ul style="list-style-type: none"> Noise Review Study Report Glare impact Assessment report Air Quality Sampling Plan

6. Materials Management

Section 6.17 in the EIA report specified the disposal of materials to the public fill reception facilities should be considered as last resorts with the preferred approach to reuse the material within the project and/or other projects.

The amounts of different types of materials generated by the activities of the Project in the month are shown in following table. The total materials quantities of the project showed that the reuse of materials was maximized and the disposal to the public filling facilities was minimized. Mitigation measures under the Waste Management Plan (WMP) revision D have been implemented during the reporting period.

Materials Type	Disposal Locations	CS-03	Total
C&D Waste	SENT	172.60 Tonnes	172.60 tonnes
	TKOSF	--	-
	TMSF	--	-
C&D Material	CWPFBP	514.20 Tonnes	514.20 tonnes
	TKOFB	--	-
Chemical Waste	Collected by licensed collector	0 Litres	0 litres
General Waste	Collected by licensed collector	--	-

7. Environmental Monitoring and Results

7.1 Monitoring Requirements

Under EP-249/2006/B condition 3.2, impact environmental monitoring including sampling, measurements and necessary remedial action should be conducted in accordance with the requirements of the EM&A Manual, which has been updated to include operational monitoring of the Ocean Park Symbio Show.

7.1.1 Construction Monitoring

Construction works at the Entry Plaza, Aqua City and Grand Aquarium under CI07 have been completed in January 2011 and, as advised to EPD on 1 April 2011 (PD/PW/GOV/151/006107), no further construction monitoring will be undertaken.

One contract at the Summit, CS03 for the Thrill Mountain and Polar Adventure is still underway. However, other than ongoing Coral Survey, no construction monitoring will be undertaken for these works, only auditing works. The audits will continue to be carried out by the Contractors ET, certified by the OPC's ET and verified by the IEC.

Terrestrial Ecology

Monitoring of the health and condition of the transplanted plant species of conservation interest should be conducted at least once a month during the first 12 month after transplantation. Proposed monitoring location would be next to the Contract CI-05 site office.

Coral

The locations of the coral monitoring stations are presented in the table below.

Coral Impact Monitoring Stations	Identity/Description
Site 1	Seaside near the Lowland
Site 2 to Site 5	Around Headland
Control Station	Between Near Round Island and Chung Hom Kok

Ocean Park Symbio Show

Operational Stage Monitoring for Ocean Park Symbio Show for Environmental Monitoring for the Symbio Show commenced on the 27 January 2011.

Air Quality monitoring was conducted at the agreed designated air quality monitoring station (AQMS) located at locations as presented in the Table below.

AQMS ID	Location	Sampling Height (m above ground)
AM1	Rooftop of Administrative Building (former Staff Quarter) in Ocean Park	10
AM2	Landscape Storage Area in Ocean Park	3
AM3	Rooftop of Main Medical Block of Graham Hospital	20

One 24-hr average RSP sample was collected on each scheduled day for monitoring by a High Volume Sampler (HVS) following the USEPA method, EPA IO-2.1. Calibration of the equipment has followed the requirements set out in EPA IO-2.1.

Noise monitoring was conducted at five designated noise monitoring locations in accordance with the approved EM&A Manual. Alternative noise monitoring had been proposed because of accessibility problem, as set out in the Table below.

Monitoring Noise Monitoring Stations	Description	Location	With or without Façade Correction
AON1	Open Area adjacent to Police Training School	1.2m above street level	Without façade correction
AON2	Old canteen building, Ocean Park	1.2m above street level	With façade correction
AON3	Orchid Valley	1.2m above street level near the entrance gate	Without façade correction
AON4	Manly Villa	1.2m above street level near the entrance	With façade correction
AON5	Hau Yuen	1.2m above street level outside boundary wall	With façade correction

Six consecutive measurements of LAeq, 5 min reading were carried out to calculate the LAeq, 30 min noise level during the Lagoon Show.

Six consecutive measurements of LAeq, 5 min reading were carried out to calculate the LAeq, 30 min noise level before the lagoon night show, ie during daily operation of the Ocean Park without the Lagoon Show.

Three consecutive measurements of LAeq, 5 min reading were carried out to calculate the LAeq, 15 min noise level after the lagoon night show, ie without operation of the Ocean Park to establish the background noise levels.

Any significant influencing factors on the measured noise levels were taken into account in accordance with standard acoustical principles and practices. The corrected noise level due to the lagoon night show and the operation of Ocean Park was computed based on the background noise level and measured noise level.

7.2 Monitoring Results

7.2.1 Construction Monitoring Results

Terrestrial Ecology

According to the requirement in the EM&A Manual, the monitoring of transplanted plants at the receptor has been completed in August 2008.

Coral

No coral monitoring survey was carried out in July 2011. The next coral monitoring survey will be carried out in August 2011.

7.2.2 Operational Stage Monitoring for Ocean Park Symbio Show

The report on the impact monitoring results for the open-air night show, which commenced on 27 January 2011, is provided at Part 3 of this report.

For Air Quality Monitoring, 24-hr average Respirable Suspended Particulates (RSP) monitoring was conducted at a designated monitoring station on the rooftop of the Administrative Building in OP (AM1) for the Landscape Storage Area (AM2), and the Roof top of the Main Medical Block of Graham Hospital (AM3) on 16 June 2011.

No exceedance of A/L Level is monitored during the reporting period.

Monitoring Location	Monitoring Date	24-hr RSP Concentration (μgm^{-3})	Action/Limit Level (μgm^{-3})
AM1 (Rooftop of Administrative Building (Old Staff Quarters in Ocean Park))	16 June 2011	27	180
AM2 (Landscape Storage Area)	16 June 2011	18	180
AM3 (Roof top of the Main Medical Block of Graham Hospital (16 June 2011	18	180

Noise Monitoring results indicated that the background corrected Lagoon Night Show Noise Levels have complied with the Limit Levels at all monitoring stations during all monitoring dates.

The background corrected Daily Operational Noise Levels have complied with the Limit Levels at most of the monitoring stations during most of the monitoring dates. Noise exceedances were recorded at AON1 (Open Area adjacent to Police Training School) due to high background noise from the visitors and traffic during public holidays and at AON3 (Woodgreen Estate) and AON5 (Hau Yuen) due to the traffic noise from Shouson Hill Road as indicated in the summary below.

Noise exceedance was also recorded at AON2 (Roof of Old Canteen Building) on 14 June 2011 due to construction works near the Cable Car terminal under CNP No GW-RS0313-11)

Summary of Daily Operational Noise Exceedance during this Reporting Period

Date	Noise Monitoring Station	<u>Measured Noise Level, dB(A)</u>		Daily Operational Noise Level (Background Corrected) ^(a) , Leq (30 min) dB(A)	Limit Level, Leq (30 min) dB(A)
		Daily Operational Noise Level, Leq (30 min) dB(A)	Background Noise Level, Leq (15 min) dB(A)		
29 May 2011 (Public holiday)	AON1	67.6	65.1	67.0	60
	AON3	64.4	61.5	61.2	55
31 May 2011 (weekday)	AON3	66.1	64.0	61.9	55
5 June 2011 (public holiday)	AON1	66.0	65.6	66.0	60
		65.7 (Lagoon Night Show noise level)	64.8	61.4 (Lagoon Night Show noise Level (Background Corrected))	60
	AON3	64.2	61.9	60.3	55
7 June 2011 (weekday)	AON3	62.7	61.2	57.4	55
12 June 2011 (public holiday)	AON1	66.9	65.8	63.5	60
14 June 2011 (weekday)	AON2	68.8 (Lagoon Night Show Noise Level)	67.1	63.7 (Lagoon Night Show Noise Level (Background Corrected))	60
	AON5	59.0	55.8	56.1	55
19 June 2011 (public holiday)	AON1	65.4	64.5	61.1	60
21 June 2011 (weekday)	AON3	66.3	64.9	60.5	55
	AON5	59.0	55.3	56.6	55

Note :

(a) The Background corrected Noise Levels were either measured in front of a façade at AON2, AON4 and AON5 or with façade correction of 3dB(A) at AON1 and AON3.

8. Site Audit

8.1 IEC Site Audit

IEC conducted monthly site audit on CS-03 on 8 July 2011. Audit checklists are attached in Appendix A of Part 1.

CS-03 Observations:

- Oil drums were placed on bare ground. The Contractor was reminded to place all oil drums in drip trays or store them in chemical storage areas.
- Stagnant water was accumulated on site after heavy rain last week. The Contractor was reminded to remove the stagnant water as soon as possible.

8.2 Non- Compliance

No non-compliances were recorded in July 2011.

9. Implementation status of Environmental Mitigation Measures

Please see Part 2, of this Report for the individual contractual reports for the details of the implementation of environmental mitigation measures.

10. Summary of Complaint, Summon or Prosecution

No complaint, summon or prosecution was recorded in the reporting month.

11. Future Issues

Key Issues to be considered in the coming month include:

CI-05

- Construction phase had ceased in early-June 2009.

CS-01

- Construction phase had ceased in mid-October 2008.

CW-02

- Construction phase had ceased in mid-February 2010.

CI-07

- Construction phase had ceased in January 2011.

CS-02

- Construction phase had ceased in April 2011.

CS-03

- Remove waste more frequently.
- Ensure drip tray to be provided for oil drum.
- Ensure water spray on haul road to avoid dusty environment.
- Ensure stockpile materials to be covered by tarpaulin or other means.
- Ensure stagnant water is removed promptly after heavy rain.

12. Conclusion and Recommendation

12.1 Conclusion

No non-compliance from IEC, complaint, summons or prosecution related to environmental issues was made against the Ocean Park Master Redevelopment Project in the reporting period of July 2011.

Daily operational noise and lagoon night show noise monitoring were carried out at five designated monitoring stations during this reporting period. Out of the 5 stations, noise exceedances were recorded at AON1 (Open Area adjacent to Police Training School) due to high background noise from the visitors and traffic during public holidays, from AON2 (Roof of Old Canteen Building) on 14 June 2011 due to construction works near the Cable Car terminal and AON3 (Woodgreen Estate) and AON5 (Hau Yuen) due to the traffic noise from Shouson Hill Road.

12.2 Recommendation

According to the environmental audit performed in the reporting month, the following recommendations are made:

Air Quality Impact

- To prohibit any open burning on site.
- To regular maintain the machinery and vehicles on site.
- To implement dust suppression measures on dry surfaces.

Noise Impact

- To inspect the noise sources from inside and outside of the site.
- To space out noisy equipment and position as far away as possible from sensitive receivers.
- To have regular maintenance of vessels and equipment used.

Water Quality Impact

- To minimize water discharge runoff into nearby water body.
- To treat site surface runoffs and wastewater generated from various construction activities with wastewater treatment system (comprised of chemical coagulation, sedimentation and pH control)
- To review and implement temporary site drainage management plan.
- Silt removal facilities, channels, manholes and wastewater treatment system should be frequently cleaned the deposited silt and grit to maintain in proper condition.
- To review the adequacy of the desilting facilities' capacity.

Waste/Chemical Management

- To check for any accumulation of waste materials or rubbish on site.
- To avoid any discharge of chemical waste or oil directly from the site.
- To regularly and properly collect, store and dispose of all waste types, including floating refuses around the silt curtain.

Operational Stage Monitoring for Ocean Park Symbio Show

Recommendation has been given to continue with noise monitoring at the same stations using the same frequency and approach during the second to the twelfth months of the operation of the open-air night show.

To satisfy potentials concerns over RSP concentrators, the number of monitoring stations has been increased to a total of 3 monitoring stations. As the monitored results are within the AQO, the frequency has been reduced to monthly.

Appendix A

Part 1 Independent Environmental Checker's Site Inspection Records

Ocean Park Master Redevelopment Project
Contract P007
Independent Environmental Checker

MONTHLY SITE INSPECTION CHECKLIST

Inspection Date	08/07/2011	Time	15:30	Inspected By	EM: L. Pickles IEC: Florence Yuen Contractor: CS03: W. Chung
Site Location	CS03				

Weather

Condition	<input checked="" type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm	<input type="checkbox"/> Hazy
Temperature	33°C		Humidity	<input checked="" type="checkbox"/> High	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input checked="" type="checkbox"/> Calm	<input type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong	Direction 		

		Close-out on last comments Y/N	N/A or not obs	Yes	No	Photo/Remarks
Construction Noise						
S2.18	Is a valid Construction Noise Permit (CNP) obtained for works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S2.26	Good Site Practices:					
	• Are the operating plants well-maintained and serviced regularly?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Are silencers or mufflers utilized on construction equipment? Are they properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Is the mobile plant sited far enough from NSRs?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Are Intermittently used machines and plants shut down between work periods?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Is the plant known to emit noise strongly in one direction, if any, oriented to direct noise away from the NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is the stockpile or other structures utilized effectively, wherever practicable, in screening noise from the works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S2.27	Are suitable quiet plants adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S2.28	Are movable barriers used for both movable PME and stationary PME?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S2.29	Do the screening materials used achieve the predicted noise reduction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S2.30	Are the noisy works avoided during examination period of the nearby school?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Blasting Noise						
S2.32	• Are the NSRs informed of the blasting work in advance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is sufficient time allowed for alerting all the potential NSRs prior to every blasting work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

- Are proper procedures put in place to alert and minimise any startling effect on the staff working in Ocean Park?

	✓		
--	---	--	--

- Is the optimal amount of charge used evaluated for noise reduction?

	✓		
--	---	--	--

Landscape and Visual

S3.10 Consideration on existing surrounding vegetation:

- Are temporary tree nurseries set up?
- Is "no-intrusion zones" implemented?
- Is the existing vegetation protected from damage?
- Are hill fire prevention measures taken?
- Is dust and erosion controlled for exposed soil?
- Are the irrigation networks set up throughout the Establishment Period?
- Is Quarterly Report on existing trees to be retained or transplanted prepared by the Contractor?

	✓		
--	---	--	--

	✓		
--	---	--	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

	✓		
--	---	--	--

	✓		
--	---	--	--

S3.11 Consideration on appearance and view:

- Is the appearance of hoardings suitable?
- Is the appearance of construction workers, plants/machines suitable?
- Are the screening and alignment of the temporary barging point and conveyor system suitable?
- Are the selected security floodlights suitable?

		✓	
--	--	---	--

		✓	
--	--	---	--

	✓		
--	---	--	--

	✓		
--	---	--	--

Ecology

S4.5 Transplantation:

- Is the transplantation work supervised by a qualified botanist/horticulturalist in the ET?
- Are the transplanted plant species of conservation interest monitored during the first 12 months after transplantation?

		✓	
--	--	---	--

		✓	
--	--	---	--

S4.7 Construction:

- Is the runoff entering watercourses avoided by control measure, especially during heavy rain?
- Is the site runoff directed to regularly cleaned and maintained silt traps (or oil separators)?
- Are sediment traps included in drainage to collect and control construction run-off?
- Is suitable size silt traps or oil Interceptor used?
- Is vegetation survey carried out to determine the feasibility and suitability of individual plants for transplantation?
- Are the trees located within the works area preserved suitably?
- Are individual plants of conservation interest transplanted prior to the construction phase?
- Are the equipments and stockpiles placed in designated works areas and access routes selected on existing disturbed land to minimise disturbance to natural habitats?

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

		✓	
--	--	---	--

- Are construction activities restricted to the work areas demarcated?

		✓	
--	--	---	--
- Are waste skips provided to collect general refuse and construction wastes?

		✓	
--	--	---	--
- Are the wastes disposed of timely and properly off-site?

		✓	
--	--	---	--
- Is open burning on works sites prohibited?

		✓	
--	--	---	--
- Are native plant species made use of as far as possible on newly formed land?

		✓	
--	--	---	--

Construction Waste

S5.4

Good Site Practices

- Are arrangements made for collection and effective disposal of all wastes generated?

		✓	
--	--	---	--
- Are the waste management and chemical handling procedures followed?

		✓	
--	--	---	--
- Are sufficient waste disposal points provided?

		✓	
--	--	---	--
- Are the wastes disposed of regularly?

		✓	
--	--	---	--
- Are appropriate measures taken to minimise windblown litter and dust during transportation of waste by either covering trucks or transporting wastes in enclosed containers?

		✓	
--	--	---	--
- Are the drainage systems, sumps and oil interceptors regularly cleaned and maintained?

		✓	
--	--	---	--

S5.5

Waste Reduction Measures:

- Is the C&D waste from demolition and decommissioning of existing facilities sorted to recover recyclable materials?

		✓	
--	--	---	--
- Are different types of wastes segregated and stored in different containers, skips or stockpiles to enhance reuse or recycling and the proper disposal?

		✓	
--	--	---	--
- Are aluminium cans segregated in labelled bins and collected by individual collectors for recycling?

		✓	
--	--	---	--
- Are proper storage and site practices maintained to minimise the potential for damage or contamination of construction material?

		✓	
--	--	---	--
- Are the construction materials planned and stocked carefully to avoid unnecessary generation of waste?

		✓	
--	--	---	--

S5.7

General Refuse

- Is the general refuse stored in enclosed bins or compaction units separate from C&D material?

		✓	
--	--	---	--
- Is the general refuse removed regularly by a waste collector?

		✓	
--	--	---	--

S5.8

C&D Material

- Are the excavated materials from site formation of the expansion areas and tunnel construction for the funicular system reused on-site as backfilling material and for landscape works?

		✓	
--	--	---	--
- Are the surplus rock and other inert C&D material disposed of at the public fill sites?

		✓	
--	--	---	--
- Is a waste management plan prepared?

		✓	
--	--	---	--
- Is a recording system present for the record of amount of wastes generated, recycled and disposed?

		✓	
--	--	---	--

	• Is the trip-ticket system required in ETWB TCW No.31/2004 followed on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S5.9	Chemical Wastes Is chemical wastes generated from the works? And if yes,	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Is the Contractor registered as a Chemical Waste Producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Are good quality containers used for separating and storing chemical wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	CS03① P1130459& P1130452
	• Are appropriate labels securely attached on each chemical waste container to indicate their corresponding chemical characteristics?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	• Is the Contractor licensed to transport and dispose of the chemical wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Land Contamination						
S6.11	• Is the contact of construction workers with contaminated materials minimised by using bulk earth-moving excavator equipment?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are appropriate cloth, personal protective equipment, hygiene and washing facilities provided to minimise exposure to any contaminated material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is stockpiling of contaminated excavated materials avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is the use of contaminated soil for landscaping without proper treatment prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are vehicles containing excavated materials covered properly to limit potential dust emissions or contaminated wastewater runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is the speed of the trucks carrying contaminated materials controlled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are the necessary waste disposal permits obtained from appropriate authorities in according with Waste Disposal (Chemical Waste) (General) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are silt removal facilities provided with retention time for silt/sand-traps of 5 minutes under maximum flow conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are the records maintained for quantity of wastes generated and disposal of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
S6.12	Remediation Process • Is biopile covered by tarpaulin or low permeable sheet to avoid dust emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Is vented air from biopile treated by blower and carbon adsorption system before released to the atmosphere?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are the materials which may generate airborne dust emissions adequately wetted prior to and during the loading, unloading and handling operations?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are silencers installed at biopile blower to minimise noise impact?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are quiet plants such as generator and blower used for biopile?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are the mixing process and other associated material handling activities properly scheduled to minimise potential noise impact?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	• Are impermeable liners placed at the bottom of biopile?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

• Is leachate collection sump construction along the perimeter of biopile?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the leachate recycled back to the biopile or truck away to Chemical Waste Treatment Centre for disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the mixing of contaminated soils and cement/water/other additive(s) undertaken at a solidification plant to minimise the potential for leaching?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is a concrete bund construction along the perimeter of the solidification/stabilisation area to prevent runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Are the loading, unloading, handling, transfer and storage of cement carried out in an enclosed system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Are the contaminated soils transported by roll-off trucks (containerisation)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is temporary hoarding provided around the treatment area to minimise the visual impact?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Air Quality

S7.23	Good Site Practices				
• Is watering carried out regularly with complete coverage to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Is watering frequently carried out for particularly dusty construction areas, temporary stockpiles and areas close to ASRs?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Are the aggregate or dusty material storage piles covered with their side enclosed to reduce emissions? Or if this is not practicable, is watering applied to aggregate fines?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is open stockpiles avoided or covered and placed far enough from the ASRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the dropping height of material restricted to minimise the fugitive dust from unloading/loading?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Is tarpaulin used to cover all dusty vehicle loads transported to, from and within the site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Are vehicle wheel and body washing facilities available at the exit points of the site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Are wind shield and dust extraction units or similar dust mitigation measures provided at the loading points? If dust generation is likely during the process, particularly in dry seasons, is water sprinklers provided at the loading site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Do the vehicles comply with the recommended speed limit of 10 km/h on unpaved roads?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Are dusty activities rescheduled during high-wind conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Are the routing of vehicles and positioning of construction plants at maximum possible distance from the ASRs?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
• Is suitable buffer zone provided and work areas fenced off with hoarding (not less than 2.4m from ground level)?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
S7.24	Drilling & Blasting				
• Is watering carried out on the exposed area after blasting?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is vacuum extraction drilling method used?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the blasting process carefully sequenced?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

	• Is the firing of explosive carried out in the morning prior to opening of the Park?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
S7.25	Crushing Plant				
	• Is water sprayed on the crusher?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Are fabric filters installed for the crushing plant?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Is chute or dust curtain used for controlling dust when transferring materials from crusher to the conveyors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
S7.26	Barging Point & Conveyor Belt System				
	• Are the conveyors placed within enclosed structures?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Is profiled steel cladding provided at two sides of loading point?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Are dust suppression sprays installed and operated at the feeding inlet and outlet?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Is the barging point placed within an enclosed structure incorporating an enclosed chute for material transfer to the barge?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
	• Is a flexible curtain hanged on the enclosed chute to prevent dust emission when excavated materials/rocks transported into the barge?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Water Quality

S8.3	Site Run-off and Drainage				
	• Are all sewer and drainage connections sealed to prevent debris, soil, sand etc. from entering public sewer before commencing any site formation work?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are temporary ditches provided to facilitate runoff discharge into appropriate watercourses, via appropriate sized silt retention pond?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are cut-off ditches provided for all major site clearance/excavation works where soils would be exposed to control runoff from the areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are channels, earth/concrete bunds and sand bags deployed to direct surface runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are catchpits and perimeter channels constructed in advance of relevant site formation works?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are the boundaries of earthworks marked and surrounded by dykes or embankments for flood protection?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are silt removal facilities, channels and manholes maintained and deposited silt/grit removed regularly to ensure that these facilities are functioning properly at all times?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are exposed soil surfaces covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Is the water pumped out from foundation excavations discharged into silt removal facilities?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are exposed soil areas minimised to reduce potential for increased siltation and contamination of runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
	• Are earthwork final surfaces well compacted and is subsequent permanent work or surface protection performed immediately?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

• Is the rainwater pumped out from trenches or excavation directed to silt removal facilities before discharge?

			✓
--	--	--	---

 CS03② P1130441

• Are open stockpiles of construction materials or construction wastes of more than 50m³ covered with tarpaulin during rainstorm?

	✓		
--	---	--	--

In case of an excavation in rainy seasons:

• Is temporary exposed slope/soil surfaces covered by tarpaulin as far as practicable?

		✓	
--	--	---	--

• Are intercepting channels provided to prevent storm runoff from washing across exposed soil surfaces?

		✓	
--	--	---	--

• Are surface protection measures and arrangements implemented to prepare for arrival of a rainstorm?

		✓	
--	--	---	--

Coral Sites

S8.4 • Are enhanced (with the use of flocculants added) sand/silt removal facilities employed for treatment of runoff from the major excavation at the Summit?

		✓	
--	--	---	--

• Is a silt curtain system used to enclose the construction phase discharge point at Tai Shue Wan?

		✓	
--	--	---	--

• Are debris and refuse collected, handled and disposed of properly to avoid entering any nearby water bodies and public drainage system?

		✓	
--	--	---	--

• Are stockpiles of cement and other construction materials kept covered when not being used?

		✓	
--	--	---	--

• Are oils and fuels used and stored in designated areas which have pollution prevention facilities (Fuel tanks and storage areas provided with locks and sited on sealed areas, within bunds of a capacity equality to 110% of the storage capacity of the largest tank)?

		✓	
--	--	---	--

• Are temporary sanitary facilities, such as portable chemical toilets, employed on-site where necessary to hand sewage from the workforce? Is a licensed contractor employed for disposal of waste matter and maintenance of these facilities?

		✓	
--	--	---	--

• Is a reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law?

		✓	
--	--	---	--

• Are aluminium cans recovered from the waste stream and collected separate labelled bins?

		✓	
--	--	---	--

• Are office wastes reduced through the recycling of paper?

		✓	
--	--	---	--

• Are training provided to workers on site cleanliness & waste management procedure?

		✓	
--	--	---	--

Cultural Heritage

S10.6 If there is any work planned within one metre of the grave, is a one metre buffer zone provided around the grave and is the grave demarcated by temporary fence?

		✓	
--	--	---	--

Hazard to Life

S11.3 Good Site Practices:

• Is the area around the magazine free of vegetation?

	✓		
--	---	--	--

• Is the control of (small) fires planned and provided through the following?

--	--	--	--

- Weekly checking of fire fighting equipment and the on-site fire water tank level.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Daily checking of all critical safety equipment on vehicle, including the fire extinguishers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Maintaining back-up means of fighting fire on the explosive vehicles.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Providing safety training for drivers and other personnel present during explosive delivery with regard to operating fire hydrants and fighting of explosive fires.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the magazine secured against unauthorised entry and theft of explosive through the following?					
- Maintaining a list of persons authorised to enter the magazine and ensuring the list is available to the magazine security guard.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Activating an alarm system that limits times at which explosive can be removed from the magazine and connecting the system to central security station.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Incorporating "Duress code" function in the alarm system.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Maintaining alarm system in good condition.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the magazine security guard located separately from the magazine complex?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the communication maintained in emergency with the following measures?					
- Providing non-hazardous electronic equipment for persons working within 60 m of detonators.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Ensuring availability of phone numbers for all key personnel.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• If there is a typhoon signal no. 3 or above, or black rainstorm signal, are all operations at magazine and transport ceased?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the risk of detonators explosion on vehicle reduced during transit through the following?					
- Ensuring that magazine within vehicle is lined.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Limiting off-site transport to 5 to 6 a.m. each day.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Escorting vehicles with separate security vehicle when using the public road.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Ensuring that UN 1.4B packaging of detonators remains intact until handed over at blasting site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the fuel isolation switch available on vehicle to prevent fire spreading in case a fire breaks out?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is an experienced driver with accident-free record employed for explosive vehicle and security escort?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Are the drivers checked for health before employing?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Are the vehicles regularly checked to maintain in good condition to reduce chance of accident due to breaking down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
• Is the truck fuel fire escalating to cause explosion avoided through the following means?					
- Ensuring that the Contractor is aware of the potential hazards to site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
- Maintaining appropriate fire fighting equipment.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

- Requiring the Contractor to plan and make emergency arrangements.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is spare/redundant fire fighting equipment provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Can communications be maintained between two vehicles (drivers and security) during the trip to prevent collision of two explosive vehicles in case of an accident?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Are the processes of checking of condition of drivers to suspend any driver of concern carried out?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Project specific measures:				
• Is the speed of vehicle limited along the Ocean Park portion of Nam Long Shan Road within 100 m of the explosives magazine to 25 km/hr?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is other contractors' use of the Ocean Park Internal service road restricted during delivery of explosives, i.e. 6 to 7 a.m?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the Ocean Park guard required to call to the magazine guard on an hourly basis when explosives are stored in magazines?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the evacuation of part or all of Ocean Park Headland Area arranged in case of the explosive magazine being engulfed in fire?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the risk to the public from accidental initiation during charging and blasting limited by the following means?				
- Closing the Ocean Park from commencement of charging holes until completion of blasting each day.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
- Arranging for relevant authorities to post notices to mariners – warning them of blasting operations and advising them to stay away from a strip 100m wide immediately to the east of Headland from commencement of charge holes until completion of blasting each day (i.e. 9 a.m).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
- Not operating amusement rides in the event of accidental explosion until confirmed free of critical damage.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• If unexploded explosives are found in blasthole(s), is the opening of Ocean Park delayed or is part of the Ocean Park delayed when there are unspent explosives?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the opportunity for arson/deliberate initiation of explosive reduced with the following means?				
- Paying attention to the security alert status from the Government.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
- Developing a security plan to address high alert level.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is an emergency plan developed to address uncontrolled fire in magazine area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the transfer of explosives between 5 to 6 a.m agreed by Mines Division?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is the road surface along the explosive transportation route maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Are the contractor's driver and security escort tested in respect of safety plan? Is the route driven before the driver undertakes the first delivery of explosives?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is adequate space provided for the explosive vehicle to manoeuvre without reversing close to the magazine to limit the likelihood of vehicle accident?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
• Is lighting for explosive vehicles provided on temporary	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

road(s)?

	✓		
--	---	--	--

S11.4 • Is ammonium nitrate emulsion (ANE) delivered outside of Park opening times?

	✓		
--	---	--	--

Observations for this month

- ① Oil drums were placed on bareground. The Contractor was reminded to place all oil drums in drip trays or store them in chemical storage area.
- ② Stagnant water was accumulated on site after heavy rain last week. The Contractor was reminded to remove it ASAP.

IEC Representative

Environmental Manager

Contractor's
Representative
CS03

Florence Yuen

(Florence Yuen)

Lindsay Pickles




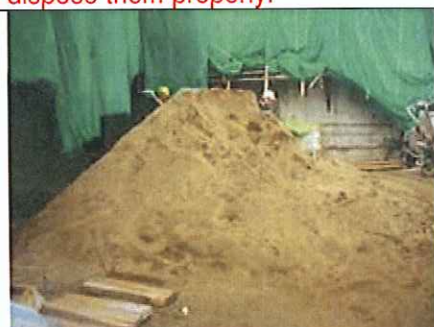

(Lindsay Pickles)

Winson Phung



(Winson Phung)

Ocean Park Master Redevelopment Project
Contract P007
Independent Environmental Checker


MONTHLY SITE INSPECTION PHOTOS

Contract CS03 Trill Mountain and Polar Adventure	
Follow up observations in June 2011	
Observation in last site inspection	Observation in this site inspection
	 
<p>P1130315: Two empty oil drums were placed on bare ground. The Contractor was reminded to place them in chemical waste storage area and dispose them properly.</p>	<p>P1130459 & P1130452: Oil drums were placed on bare ground. The Contractor was reminded either to provide drip trays to the oil drums or store them in the chemical storage area.</p>
	
<p>P1130314: An idled stockpile of dusty construction material was not covered by any means. The Contractor was reminded to cover it with tarpaulin sheets or other means to suppress dust.</p>	<p>Closed - P1130416: The idled stockpile of dusty construction material had been covered with tarpaulin sheets to suppress dust.</p>

Ocean Park Master Redevelopment Project
Contract P007
Independent Environmental Checker
MONTHLY SITE INSPECTION PHOTOS

	
<p>P1130316: Stagnant water was accumulated on site after heavy rain. The Contractor was reminded to remove them as soon as possible.</p>	<p>P1130446: Stagnant water was accumulated on site after heavy rain last week. The Contractor was reminded to remove them as soon as possible.</p>

Part 2 CS-03 EM&A REPORT (July 2011)

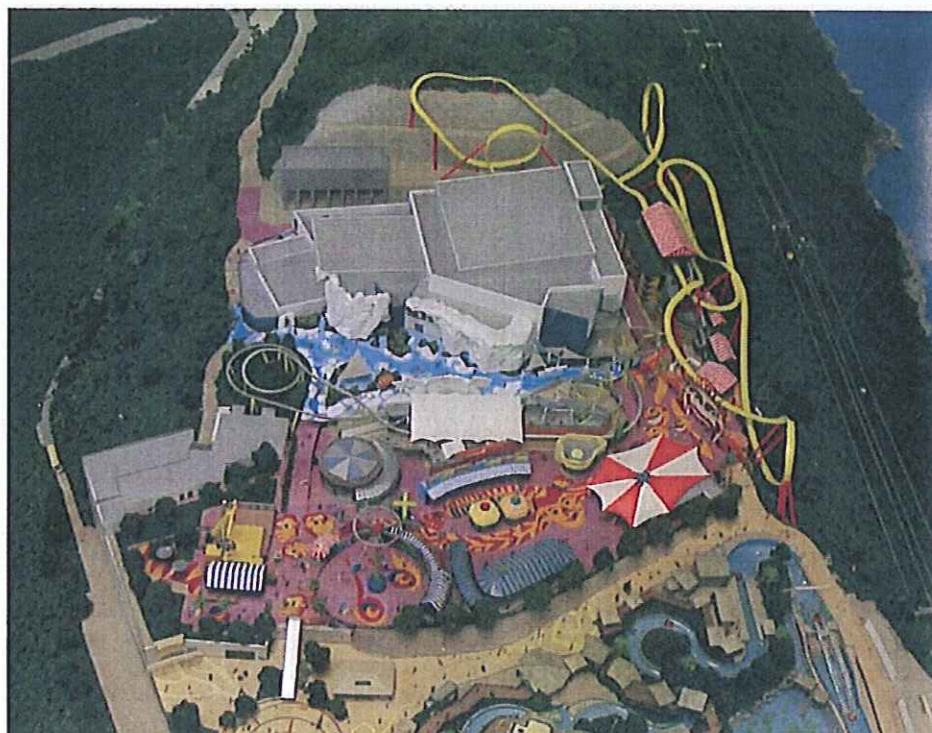

Contract No. CS03

**Ocean Park Redevelopment Project
- Thrill Mountain & Polar Adventure**

Monthly EM&A Report

July 2011

Prepared By Alex Enagnon Gbaguidi

Certified By

A handwritten signature in black ink, appearing to be 'Hui Sui Wah'.

(Hui Sui Wah)

(Senior Construction Manager)

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	1
1. INTRODUCTION	3
Background	3
Project Organizations	3
Construction Programme.....	4
Summary of EM&A Requirements	4
2. ENVIRONMENTAL AUDIT.....	5
Environmental Site Audits	5
Status of Environmental Licensing and Permitting.....	6
Status of Waste Management	6
Implementation Status of Environmental Mitigation Measures.....	7
Summary of Exceedances.....	7
Implementation Status of Event Action Plans.....	8
Summary of Complaints and Prosecutions	8
3. FUTURE KEY ISSUES	8
Key Issues for the Coming Month.....	8
4. CONCLUSIONS AND RECOMMENDATIONS	8
Conclusions	8
Recommendations	8

LIST OF FIGURE

Figure 1.1 Site Layout Plan

LIST OF APPENDICES

A Site Audit Summary

LIST OF TABLES

Table 1.1 Key Project Contacts
Table 2.1 Observations and Recommendations of Site Audits
Table 2.2 Summary of Environmental Licensing and Permit Status
Table 2.3 Actual Quantity of Waste Generated in July 2011

EXECUTIVE SUMMARY

Introduction

This is the 14th monthly Environmental Monitoring and Audit (EM&A) Report prepared by Kaden – ATAL JV for the Contract No. CS03 “Ocean Park Redevelopment Project – Thrill Mountain & Polar Adventure” (hereinafter called “the Project”). The Project was commenced on 2nd November 2009. This document reports the findings of the environmental auditing works conducted in July 2011.

The major site activities undertaken in the reporting month included:

- Construction of Tuxedos Restaurant at South Pole;
- Apply waterproofing membrane and carry out water test for roof of North Pole;
- Construction of Bobsled Station superstructure and installation of rides;
- Erection of structure steel works for Thrill Mountain;
- Carry out wall finishing works for PA Building;
- Apply waterproofing at roof of PA Building;
- Trail Run of Floorless Coaster;
- Wet trade work at Floorless Coaster;
- Apply waterproofing at roof of Floorless Coaster;
- Installation of theme works and
- Disposal Existing Stockpile.

Environmental Monitoring and Audit Works

Environmental monitoring and audit works for the Project was performed as stipulated in the updated EM&A Manual. Site audits were conducted once per week. Environmental site audits were conducted on 8th, 15th, 22nd & 29th July 2011 and the environmental ICE monthly site inspection was conducted on 8th July 2011 and No non-compliance was observed during the site audits.

The implementation of the environmental mitigation measures was checked and the environmental management plan was submitted.

No notification of exceedance was received from the Assistance Project Environmental Team Leader (ETL) in the reporting month.

Environmental Licenses and Permits

Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Redevelopment Project, Construction Noise Permit (CNP), Billing Account for Disposal of Construction Waste and Water Discharge License

Registration of Waste Producer (Chemical Waste), and notification pursuant to Section 3(1) of the Air Pollution Control (Construction Dust) Regulation was acknowledged by EPD.

Complaints and Prosecutions

No environmental complaint and prosecution was received in the reporting month.

Future Key Issues

Key issues to be considered in the coming month include:

- Wet trade work at Floorless Coaster;
- Installation of Ride Track at Bobsled Station;
- Installation of track at Bumper Blaster;
- Internal Finishing Works at PA Building;
- Erection of structural steel for Floorless Coaster workshop;
- Erection of structural steel for Aviator;
- Erection of structural steel for one side game booth;
- Erection of structural steel for four side game booth;
- Erection of structural steel for dinner hall and food kiosk;
- Internal Finishing Works for dinner hall and food kiosk;
- Installation of theme works.

1. INTRODUCTION

Background

- 1.1 Kaden-ATAL JV (the Contractor) was commissioned by the Employer to undertake the construction of the Contract No. CS03 “Ocean Park Redevelopment Project – Thrill Mountain & Polar Adventure” (the Project) and the project was commenced on 2nd November 2009. The site layout plan is illustrated in Figure 1.1.
- 1.2 These report summaries the environmental monitoring and audit works for the Project in the month of July 2011.
- 1.3 The scope of works for the Project includes:
- (a) Construction of summit reservoir and associated pump room.
 - (b) Construction of vehicular bridge.
 - (c) Construction of the Polar Adventure Building.
 - (d) Construction of back of house facilities in the Polar Adventure Building.
 - (e) Construction of other one to three storey buildings in Polar Adventure.
 - (f) Construction of foundation and installation of Bobsled Ride.
 - (g) Installation of Life Support Systems.
 - (h) Construction of one to three storey buildings in Thrill Mountain.
 - (i) Construction of foundation and installation of the Floorless Coaster.
 - (j) Installation of the Ultramax, Aviator, Musik Express and Bumper Car.
 - (k) New roadwork, paving, footpaths and infrastructure support.
 - (l) Installation of building services.
 - (m) Soft and hard landscape works.
 - (n) Construction of underground utilities and services.
 - (o) Construction of earth retaining structures.
 - (p) Construction of all interior fitting out works.
 - (q) Supply and installation of all elevator(s) and escalator(s).
 - (r) Coral survey and maintenance of existing suit curtain.

Project Organizations

- 1.4 Different parties with different levels of involvement in the project organization include:
- The Engineer and Project Environmental Team Leader (ETL) – AECOM Consultant Ltd.
 - Contractor – Kaden-ATAL JV.
 - Independent Environmental Checker (IEC) – Mott MacDonald HK Ltd.
- 1.5 The responsibilities of respective parties are provided in Section the Contractor’s EM&A Manual of the Project.
- 1.6 The key contacts of the Project are shown in **Table 1.1**.
-

Table 1.1 Key Project Contacts

Party	Name	Role	Phone No.	Fax No.
Project ET	Mr. Tommy Lau	RSS Representative (Safety & Environmental)	2552 1546	2552 1406
Contractor	Mr. Keith Kwan	Acting Project Manager	3582 6099	3582 4877
	Mr. Eric Wong	Construction Manager	3582 6005	
Contractor's ET	Mr. Alex Enagnon Gbaguidi	Contractor's Assistance Environmental Team Leader	3582 4880	3582 4877
IEC	Miss Florence Yuen	Independent Environmental Checker (IEC) Representative	2828 5757	28271823

Construction Programme

1.7 The site activities undertaken in the reporting month were:

- Construction of Tuxedos Restaurant at South Pole;
- Apply waterproofing membrane and carry out water test for roof of North Pole;
- Construction of Bobsled Station superstructure and installation of rides;
- Erection of structure steel works for Thrill Mountain;
- Carry out wall finishing works for PA Building;
- Apply waterproofing at roof of PA Building;
- Trail Run of Floorless Coaster;
- Wet trade work at Floorless Coaster;
- Apply waterproofing at roof of Floorless Coaster;
- Installation of theme works and
- Disposal Existing Stockpile.

Summary of EM&A Requirements

1.8 The EM&A programme requires construction phase environmental site audit. The duties and responsibilities comprise the following:

- monitor various environmental parameters, if necessary, as specified in the Contractor's EM&A Manual;
- analyze the environmental monitoring and audit data;
- review the EM&A programme to confirm the adequacy of mitigation measures implemented and the validity of the EIA predictions and to identify and adverse environmental impacts arising;
- carry out site inspection to investigate and audit the Contractor's site practice, equipment and work methodologies with respect to pollution control and environmental mitigation, and effect proactive action to pre-empt problems;

- audit and prepare EM&A reports on the site environmental conditions;
- report the environmental audit results to the Contractor;
- recommend appropriate mitigation measures to the Contractor in case of exceedance of Action and Limit Levels in accordance with the Event and Action Plans; and
- adhere to the procedures for carrying out complaint investigation in accordance with the Contractor's EM&A Manual.

1.9 This report presents the environmental monitoring and audit works for the Project in July 2011.

2. ENVIRONMENTAL AUDIT

Environmental Site Audits

- 2.1 Environmental site audits were carried out on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 2.2 Site audits for the Project in the reporting month were conducted on Environmental site audits were conducted on 8th, 15th, 22nd & 29th July 2011 and the environmental ICE monthly site inspection was conducted on 8th July 2011 and No non-compliance was observed during the site audits. No non-compliance was observed during the site audits. The summaries of site audits are attached in Appendix A.
- 2.3 During site inspections in the reporting month, no non-conformance was identified. The observations and recommendations are summarized in **Table 2.1**.

Table 2.1 Observations and Recommendations of Site Audits

Parameters	Date	Observations / Recommendations	Remediation/ Follow up
Waste/ Chemical Management	8/07/11	Oil drums were placed on bareground.	Remove empty oil drum off site immediately.
	8/07/11	Stagnant water was accumulated on site after heavy rain.	Remove stagnant water immediately.
Dust Control	15/07/11	An idled stockpile near Bobsled station was not covered with tarpaulin sheet or other means.	Stockpiles were covered with tarpaulin sheet.
	22/07/11	Some part of the haul road was dry.	Provide water spray regularly to suppress dust.
Air Pollution	8/7/11	N/A	

Status of Environmental Licensing and Permitting

2.4 All valid permits/licenses obtained for the Project are summarized in Table 2.2.

Table 2.2 Summary of Environmental Licensing and Permit Status

Permit No.	Valid Period		Details	Status
	From	To		
Environmental Permit				
EP-249/2006/A	23/10/2006	N/A	Expansion of the existing Ocean Park and reconstruction / modification of its existing facilities.	Valid
Registration of Chemical Waste Producer				
WPN5213-176-K2880-02	25/11/2009	N/A	Waste Disposal (Chemical Waste) (General) Regulation - Registration of Waste Producer	Valid
Construction Noise Permit				
GW-RS0516-11	09/06/2011	30/11/2011	Construction Noise Permit for Top of Nam Long Shan Rd., Ocean Park, 180 Wong Chuk Hang, Hong Kong	Valid
Water Discharge License				
WT00005926-2010	05/11/2009	28/02/2015	Discharge of industrial trade effluent arising from the Sedimentation tank at the construction site (CS03 Ocean Park Redevelopment Project) to communal storm water drain.	Valid
Others				
311433	N/A	N/A	Notification Pursuant to Section 3(1) of the Air Pollution Control (Construction Dust) Regulation	Valid
7009695	N/A	N/A	Construction Waste Disposal Billing Account with EPD	Valid

Status of Waste Management

2.5 The amount of waste generated by the construction activities of the Project in the reporting month is attached in Table 2.3.

Table 2.3 Actual Quantity of Waste Generated in July 2011

Waste Type	Examples	Actual quantity disposed (Tonnes / Liter)	Disposal Locations
C&D Waste	Construction waste (Plastic, wood and bamboo)	172.6 (T)	SENT Landfill
	Mixed rock & soil	514.2 (T)	CW barging point
Chemical waste	Used oil, spent solvent	0 L	Collected by licensed collector.

Implementation Status of Environmental Mitigation Measures

- 2.6 During site inspections in the month, the following observations and recommendations were made.

Water Quality Mitigation Measures

- The wastewater was recycled for wheel washing and dust control and Septic Tank should be maintained well functioning.

Air Quality Mitigation Measures

- The Contractor to ensure cement materials was well covered.
- The Contractor to ensure water spray was carrying out during breaking of rocks.
- The Contractor was reminded to cover the existing stockpile general fill material when they were not in use.

Noise

- No violation was observed nor recorded.

Ecology

- No violation was observed nor recorded.

Waste / Chemical Management

- Stagnant water was accumulated in drip tray. Contractor to ensure all contaminated water was well collected and stored in chemical waste storage area without spillage.
- Oil drums were observed without drip tray and place on the ground. Ensure no spillage of the chemical oil and provide trip tray accordingly.
- Collection of waste oil by registered waste collector.

Others

- No other violation was observed nor recorded.

Summary of Exceedances

- 2.7 No Action/Limit Level exceedance was reported in the reporting month.

Implementation Status of Event Action Plans

- 2.8 No complaint, summons or prosecution related to environmental issues was received or made against the Project in the reporting month.

Summary of Complaints and Prosecutions

- 2.9 No environmental complaint and prosecution related to the Project works was received during the reporting month.

3. FUTURE KEY ISSUES

Key Issues for the Coming Month

- 3.1 Key issues to be considered in the coming month include:

- Wet trade work at Floorless Coaster;
- Installation of Ride Track at Bobsled Station;
- Installation of track at Bumper Blaster;
- Internal Finishing Works at PA Building;
- Erection of structural steel for Floorless Coaster workshop;
- Erection of structural steel for Aviator;
- Erection of structural steel for one side game booth;
- Erection of structural steel for four side game booth;
- Erection of structural steel for dinner hall and food kiosk;
- Internal Finishing Works for dinner hall and food kiosk;
- Installation of theme works.

4. CONSTRUCTION OF DRAINAGE, SEWERAGE AND WATER MAIN SYSTEM.CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 4.1 Four environmental site audits were performed in July 2011. No non-compliance was observed during the site audits.
- 4.2 No exceedance of environmental monitoring was reported in the reporting month.
- 4.3 No environmental complaint and prosecution related to the project was received in the reporting month.

Recommendations

- 4.4 According to the environmental audits performed in the reporting month, the

following recommendations are suggested:

Water Quality Impact

- Should ensure that the sedimentation tank is well function before discharging waste water off site.

Dust Impact

- To carry out routine water spray to all haul roads and during rock breaking activity.
- To cover the existing stockpile general fill material when they were not in use.
- To ensure auto water spray head is on when the floor is dry and dusty.

Waste / Chemical Waste Impact

- To carry out routine inspection for chemical waste storage area after rainy day.
- To ensure spent oil keep in dip tray during drilling rig maintenance.
- To ensure all domestic waste was fully cover in rubbish bin and cleaning up frequently.
- To ensure general refuse were store in the enclosed container or compaction units and separate from C& D materials.

Air Pollution Impact

- To ensure all plants and equipments are well maintained in good condition and replace air filter frequently.

Site Layout Plan

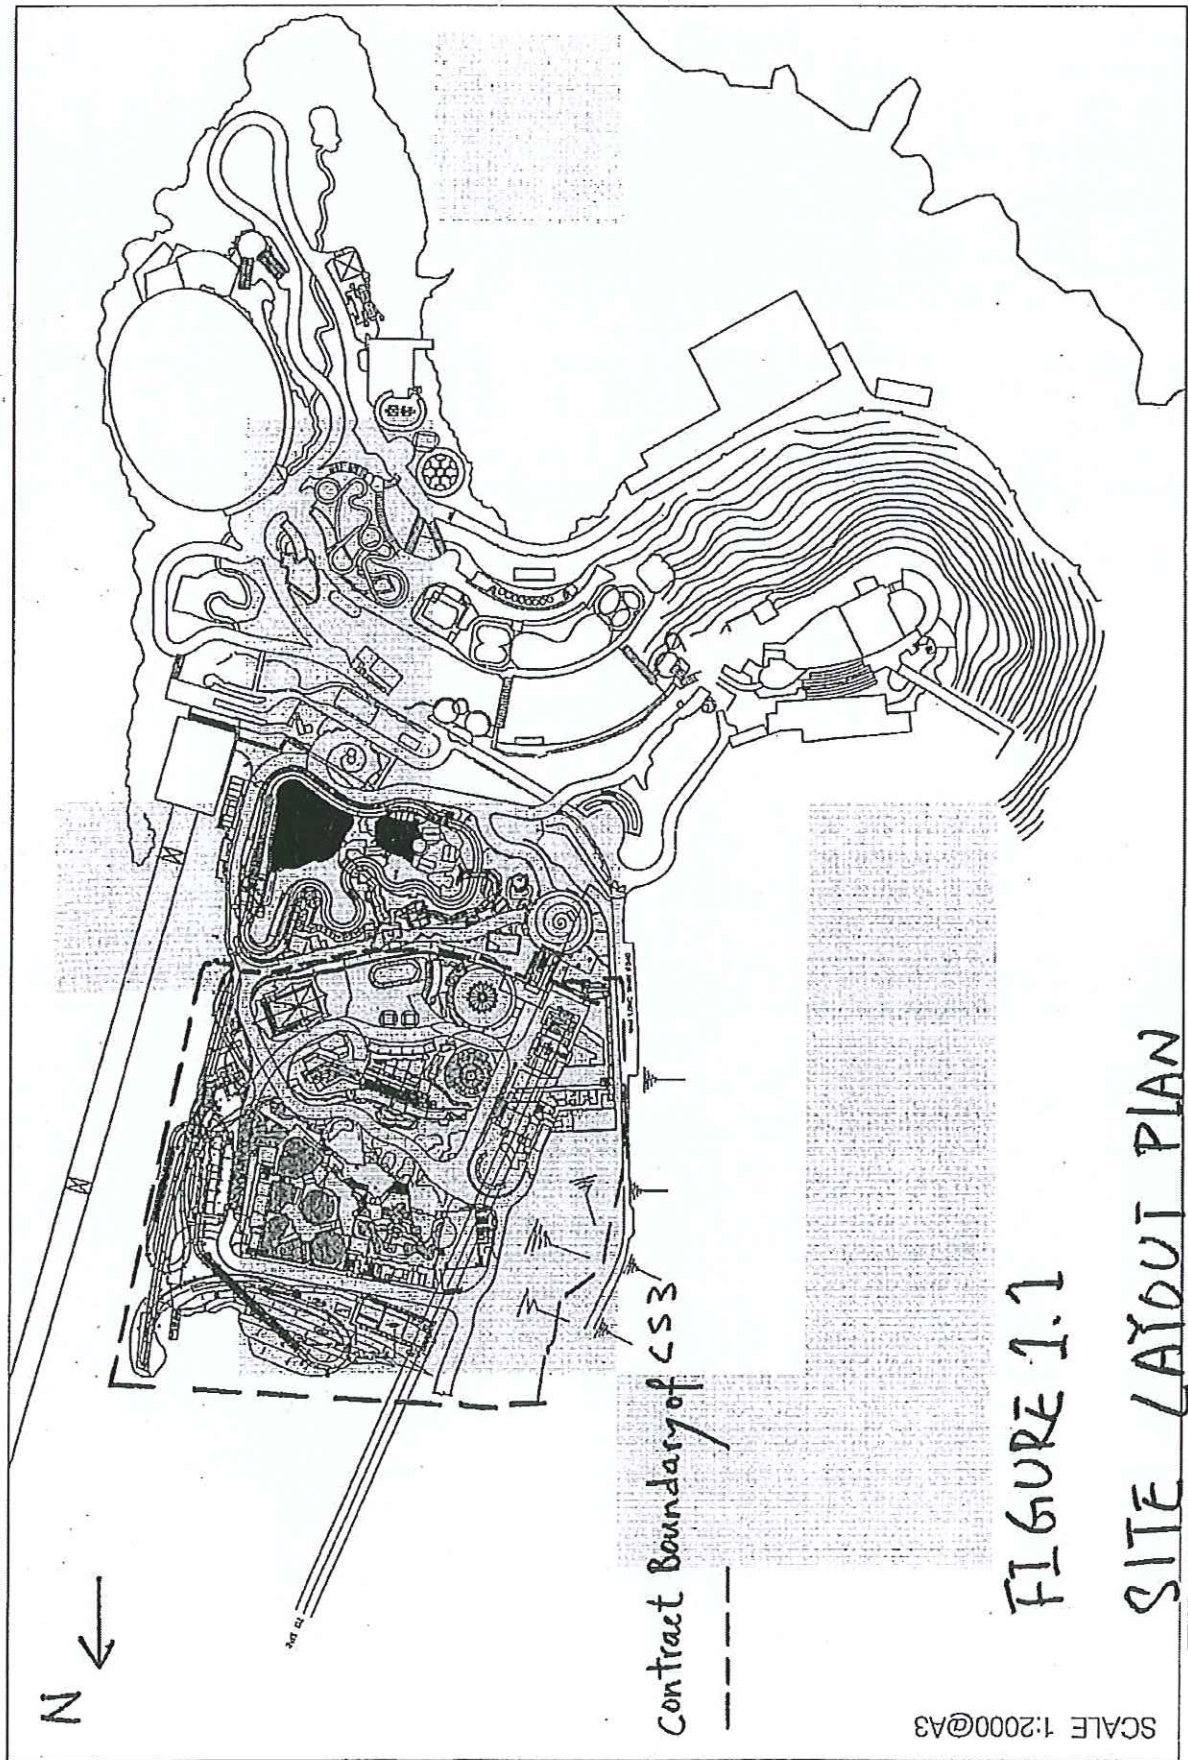


FIGURE 1.1

SITE LAYOUT PLAN

APPENDIX A
Site Audit Summary
(refer to Appendix A of EM & A Report)

**Part 3 Ocean Park Symbio Show
5th Monthly Monitoring Report**

Ocean Park Corporation, Hong Kong

Ocean Park Symbio Show:
*5th Air Quality and Noise Monitoring
Report*

July 2011

Environmental Resources Management

21/F Lincoln House
979 King's Road
Taikoo Place
Island East, Hong Kong
Telephone: (852) 2271 3000
Facsimile: (852) 2723 5660
E-mail: post.hk@erm.com
<http://www.erm.com>

Ocean Park Corporation, Hong Kong

Ocean Park Symbio Show:
*5th Air Quality and Noise Monitoring
Report*

July 2011

Reference 0128330

For and on behalf of
ERM-Hong Kong, Limited

Approved by: Frank Wan

Signed: 

Position: Partner

Date: 12 July 2011

CONTENTS

1	INTRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	AIR QUALITY MONITORING	2
2.1	INTRODUCTION	2
2.2	SAMPLING METHODOLOGY	2
2.3	MONITORING RESULTS	3
3	NOISE MONITORING	5
3.1	INTRODUCTION	5
3.2	NOISE MONITORING REQUIREMENTS	5
3.3	RESULTS OF NOISE MONITORING	8
3.4	SUMMARY OF NOISE EXCEEDANCES	8
4	OVERALL CONCLUSIONS	11

ANNEXES

<i>Annex A1</i>	<i>Calibration Record</i>
<i>Annex A2</i>	<i>Laboratory Report</i>
<i>Annex A3</i>	<i>Detailed Summary and Graphical Presentation of the Cumulative Results Since Commencement of Open-air Night Show</i>
<i>Annex A4</i>	<i>Recorded RSP Concentrations at EPD's AQMSs in Tung Chung, Shatin, Tai Po, Yuen Long, and Tap Mun on 16 June 2011</i>
<i>Annex A5</i>	<i>Recorded Weather Data at HKO's Weather Station in Wong Chuk Hang on 16 June 2011</i>
<i>Annex B1</i>	<i>Calibration Certificates of the Noise Measurement Equipment</i>
<i>Annex B2</i>	<i>Results of Noise Monitoring</i>
<i>Annex B3</i>	<i>Graphical Presentation of Noise Monitoring Results</i>
<i>Annex B4</i>	<i>Construction Noise Permit</i>

ERM-Hong Kong, Limited (ERM) has been appointed by Ocean Park Corporation (OPC) to undertake air quality and noise monitoring for the first operational year of the Open-air Night Show under the "*Repositioning and Long Term Operation Plan of Ocean Park*" (the Project).

1.1 PURPOSE OF THE REPORT

The Open-air Night Show commenced on 27 January 2011. This is the 5th air quality and noise monitoring report which summarises the impact monitoring results during the reporting period from 27 May to 26 June 2011.

1.2 STRUCTURE OF THE REPORT

After this introductory section, the remainder of this report is arranged as follows:

Section 2 describes the air quality sampling methodology, presents the monitoring results and discusses the results;

Section 3 describes the noise monitoring methodology, presents the monitoring results and discusses the results;

Section 4 presents an overall conclusion of the air quality and noise monitoring.

2.1 INTRODUCTION

In accordance with Clause 2.31 of the Environmental Permit (EP), an updated air quality monitoring programme shall be developed as part of the updated EM&A Manual for the measurement of air quality impact (in terms of respirable suspended particulates, RSP) during the first operational year of the Open-air Night Show and for submission to the Director of Environmental Protection (DEP) in January 2011. The air quality monitoring has been carried out based on the requirements given in the updated air quality monitoring programme.

2.2 SAMPLING METHODOLOGY

2.2.1 Sampling Parameters and Frequency

In accordance with the updated air quality monitoring programme, 24-hr average RSP levels should be monitored on a weekly basis in the first month of the Open-air Night Show. If the monitored results in the first month complied with Action/Limit (A/L) Level, the frequency should be reduced to a monthly interval for the rest of eleven months in the first operational year. Monitoring of the 24-hr average RSP has commenced at AM1 in the 1st reporting month and at AM2 and AM3 in the 3rd reporting month. Monthly monitoring of 24-hr average RSP was taken at AM1, AM2 and AM3 on 16 June 2011.

2.2.2 Sampling Locations

Air quality monitoring was conducted at three designated air quality monitoring station (AQMS) as presented in *Table 2.1* and illustrated in *Figure 2.1*.

Table 2.1 Air Quality Monitoring Station

AQMS ID	Location	Sampling Height (m above ground)
AM1	Rooftop of Administrative Building (Former Staff Quarters) in Ocean Park	10
AM2	Landscape Storage Area in Ocean Park	3
AM3	Rooftop of Main Medical Block of Graham Hospital	20

2.2.3 Sampling and Laboratory Analysis Methodology

One 24-hr average RSP sample was collected on each scheduled day by a High Volume Sampler (HVS) following the USEPA method, EPA IO-2.1. Calibration of the equipment has followed the requirements set out in EPA IO-2.1 with the calibration record given in *Annex A1*. A summary of the sampling methodology and equipment is presented in *Table 2.2*.

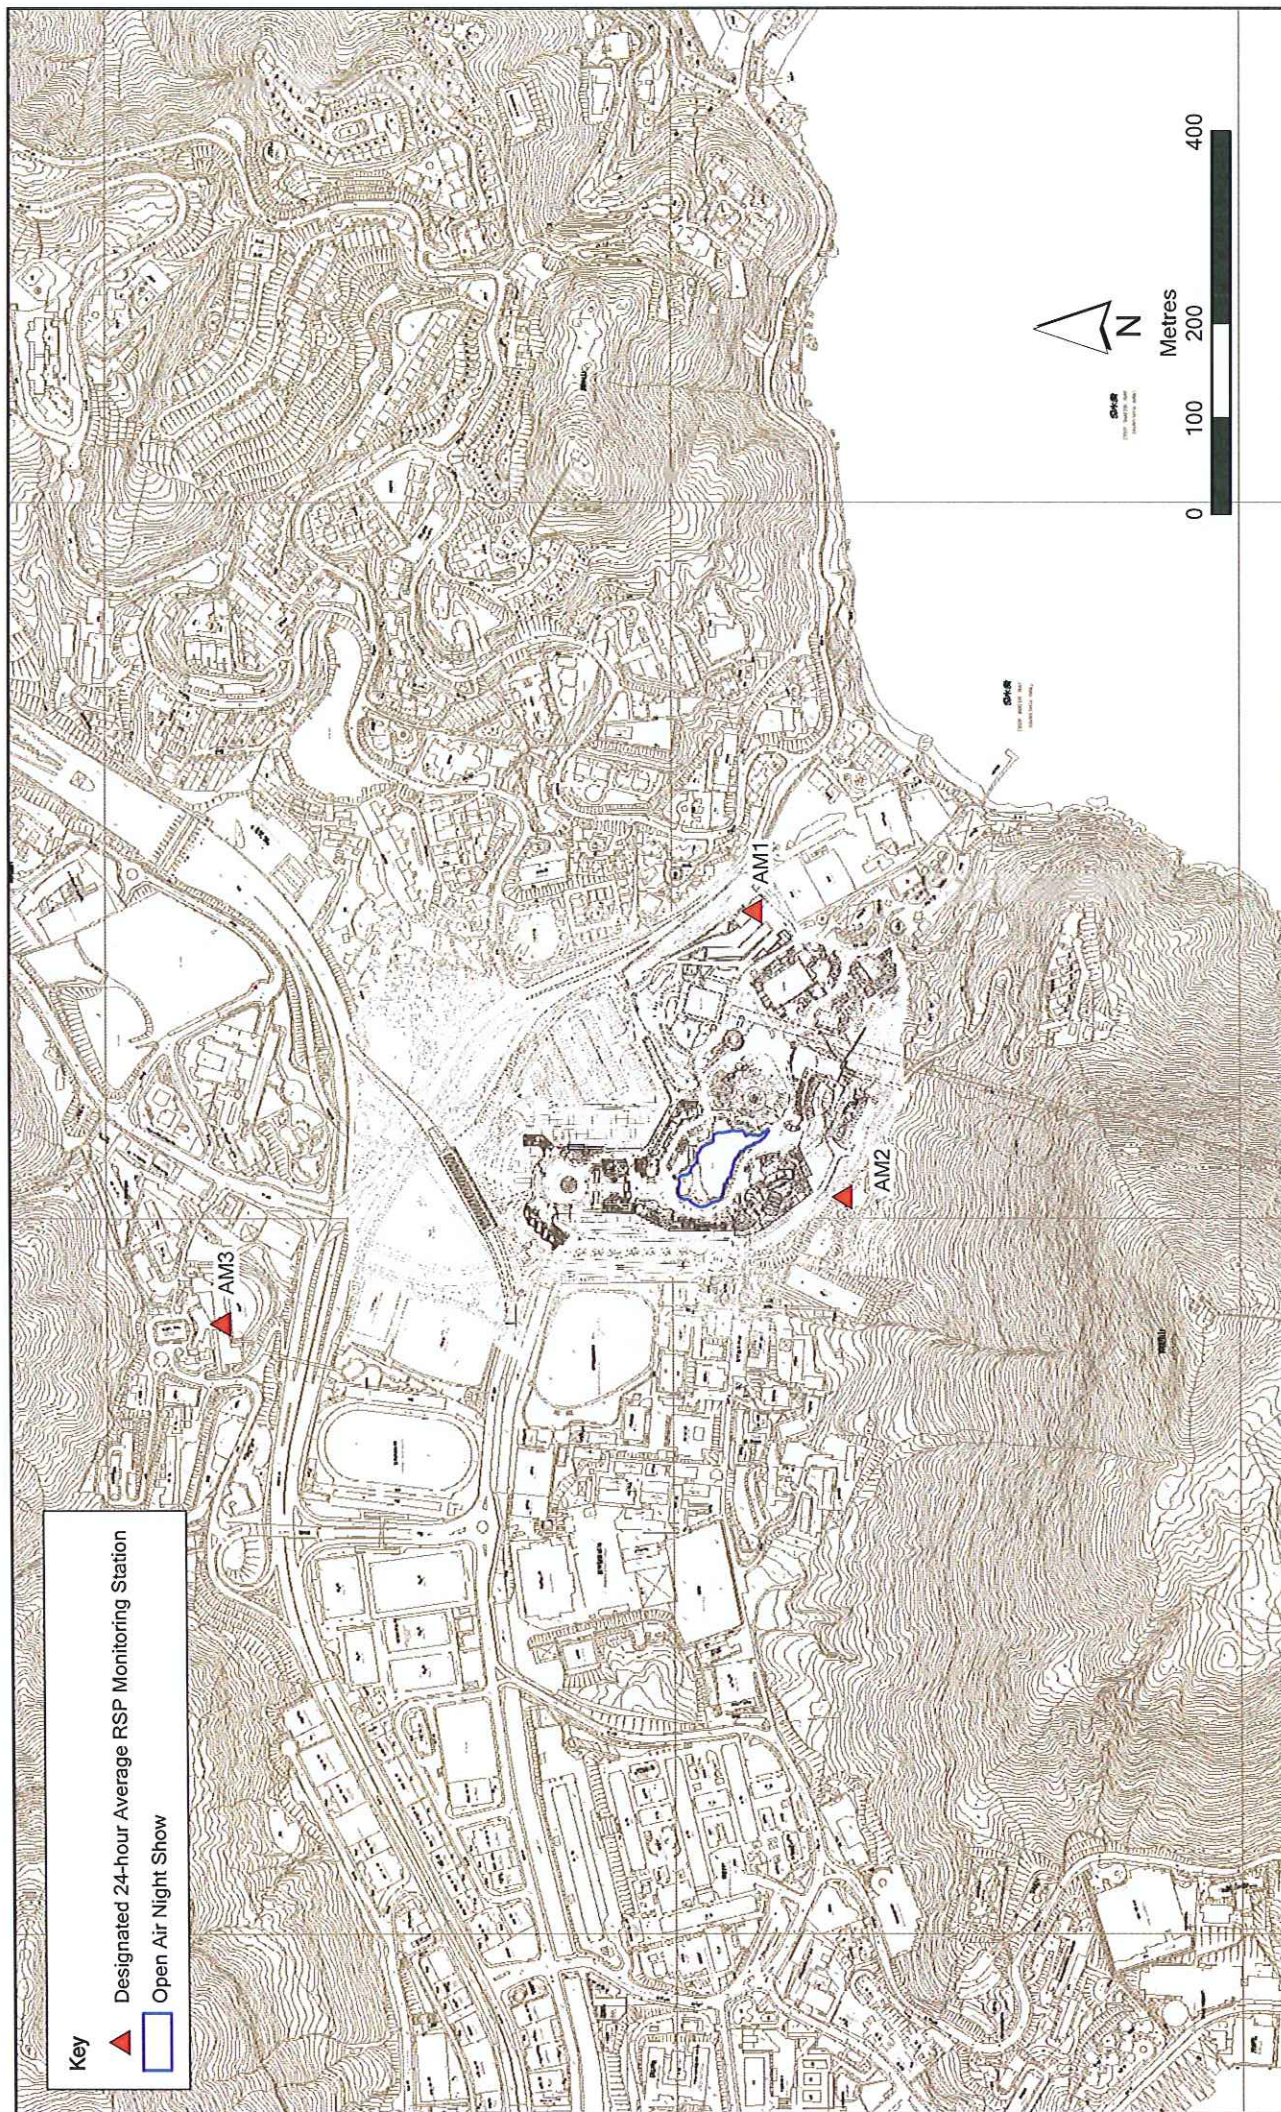


Figure 2.1

Designated 24-hour Average RSP Monitoring Stations during Operation of Open Air Night Show

Table 2.2 *Summary of Sampling and Laboratory Analysis Method*

Sampling Parameter	Method	Equipment
24-hr average RSP	EPA IO-2.1	High volume sampler

2.2.4 *Sampling Period*

The sampling periods at AM1, AM2 and AM3 are summarized in *Table 2.3*.

Table 2.3 *Sampling Period*

Sampling Parameter	Sampling Period	AQMS
24-hr average RSP	17:00 (16 June 2011) – 17:00 (17 June 2011)	AM1, AM2, AM3

2.2.5 *Compliance Assessment*

The measured 24-hr average RSP concentrations have been compared with the Action/Limit Level (A/L Level) which is the 24-hr average AQO for RSP (180 μgm^{-3}). Should exceedance of A/L Level occur, actions summarized in the Event and Action Plan (*Table 7.5* of updated EM&A Manual) should be followed.

2.3 *MONITORING RESULTS*

The 24-hour average RSP concentrations monitored at AM1, AM2 and AM3 are summarized in *Table 2.4*. The detailed laboratory report is presented in *Annex A2*.

Table 2.4 *24-hr Average RSP Monitoring Results*

Monitoring Location	Monitoring Date	24-hr RSP Concentration (μgm^{-3})	Action/Limit Level (μgm^{-3})
AM1 (Rooftop of Administrative Building (Old Staff Quarters) in Ocean Park)	16 June 2011	27	180
AM2 (Landscape Storage Area in Ocean Park)	16 June 2011	18	180
AM3 (Rooftop of Main Medical Block of Graham Hospital)	16 June 2011	18	180

All measured 24-hour average RSP concentrations have been well below the A/L Level (ie, 180 μgm^{-3}). Detailed summary of the air quality monitoring data and graphical presentation of the cumulative results since the commencement of Open-air Night Show are given in *Annex A3*.

The average 24-hour average RSP concentrations during the Open-air Night Show time measured at five EPD air quality monitoring stations (AQMSs) at Tung Chung, Shatin, Tai Po, Yuen Long and Tap Mun were also provided as a reference (See *Annex A4*).

The 24-hour average background RSP concentrations measured at the 5 EPD stations were between 2.2 and 31.9 $\mu\text{g m}^{-3}$ during the reporting period. The monitored 24-hr average RSP concentrations at AM1, AM2 and AM3 have been compared with those measured at the EPD's AQMSs during the same monitoring periods. The measured results are comparable with the background concentrations and well below the A/L Level.

Wind data (including wind directions and speeds), ambient temperature and relative humidity measured at Wong Chuk Hang weather station operated by the Hong Kong Observatory (HKO) were also provided in *Annex A5* as reference.

3.1 INTRODUCTION

Noise monitoring has been carried out following the requirements given in the updated EM&A Manual. The requirements and results are detailed in the following sections.

3.2 NOISE MONITORING REQUIREMENTS

It has been recommended in the EIA Report for *"Repositioning and Long Term Operation Plan of Ocean Park"* and stated in the EM&A Manual that fixed plant noise source monitoring should be conducted during the first operational year of the Open-air Night Show at the Aqua City.

The monitoring of fixed plant noise source impact is to be conducted:

- During the lagoon night show (hereinafter referred to as "lagoon night show noise monitoring")
- Not during the lagoon night show (hereinafter referred to as "daily operational noise monitoring")

Lagoon night show noise monitoring was carried out at all designated monitoring stations during the performance of lagoon night shows at a logging interval of 30 minutes. The noise monitoring was conducted twice a week, i.e. once on a normal weekday and once on a general holiday or Sunday.

The need for noise monitoring during the lagoon night show was reviewed based on the monitoring results, any requirements to adjust the loudspeaker system, and any change to the show schedule or rundown. With the same loudspeaker system and show rundown, if the noise levels of the month comply with the fixed plant noise criteria as stipulated in *Technical Memorandum on Environmental Impact Assessment Process (EIAO-TM)*, or are consistent with the baseline noise levels, the ETL may consider not including the noise monitoring in the subsequent monitoring programme. Agreement from the IEC and approval from EPD must be sought prior to suspension of noise monitoring. Impact monitoring can be resumed if there is any change to the power, orientation, and volume of the loudspeaker system, or to the show rundown, or an increase of show frequency.

For daily operational noise monitoring, 30-minute average noise measurement at each designated station during the operational hours of Ocean Park but not during the lagoon night show should be conducted. The monitoring frequency should be the same as that for the noise monitoring during the

lagoon night show. Agreement from the IEC and approval from EPD must be obtained prior to suspension of noise monitoring.

The following sections describe the detailed methodology of the fixed plant noise monitoring.

3.2.1 *Monitoring Locations*

Noise monitoring was conducted at five designated noise monitoring locations in accordance with the approved EM&A Manual. Alternative noise monitoring has been proposed because of accessibility problem, as presented in Table 3.1, and shown in Figure 3.1.

Table 3.1 *Alternative Noise Monitoring Stations during the Operational Phase*

Alternative Noise Monitoring Stations	Description	Location	With or without Façade Correction
AON1	Open Area adjacent to Police Training School	1.2m above street level	without facade correction
AON2	Old canteen building, Ocean Park	1.2m above roof level	with facade correction
AON3	Woodgreen Estate	1.2m above street level outside boundary wall	with facade correction
AON4	Manly Villa	1.2m above street level near the entrance	with facade correction
AON5	Hau Yuen	1.2m above street level outside boundary wall	with façade correction

3.2.2 *Monitoring Parameters*

Lagoon Night Show Noise Monitoring

Six consecutive measurements of $L_{Aeq, 5 \text{ min}}$ reading were carried out to calculate the $L_{Aeq, 30 \text{ min}}$ noise level during the lagoon night show.

Daily Operational Noise Monitoring

Six consecutive measurements of $L_{Aeq, 5 \text{ min}}$ reading were carried out to calculate the $L_{Aeq, 30 \text{ min}}$ noise level before the lagoon night show, ie during operation of the Ocean Park.

Background Noise Level

Three consecutive measurements of $L_{Aeq, 5 \text{ min}}$ reading were carried out to calculate the $L_{Aeq, 15 \text{ min}}$ noise level after the lagoon night show, ie without operation of the Ocean Park.

Any significant influencing factors on the measured noise levels were taken into account in accordance with standard acoustical principles and practices. The corrected noise level due to the lagoon night show and the operation of Ocean Park was computed based on the background noise level and measured noise level.

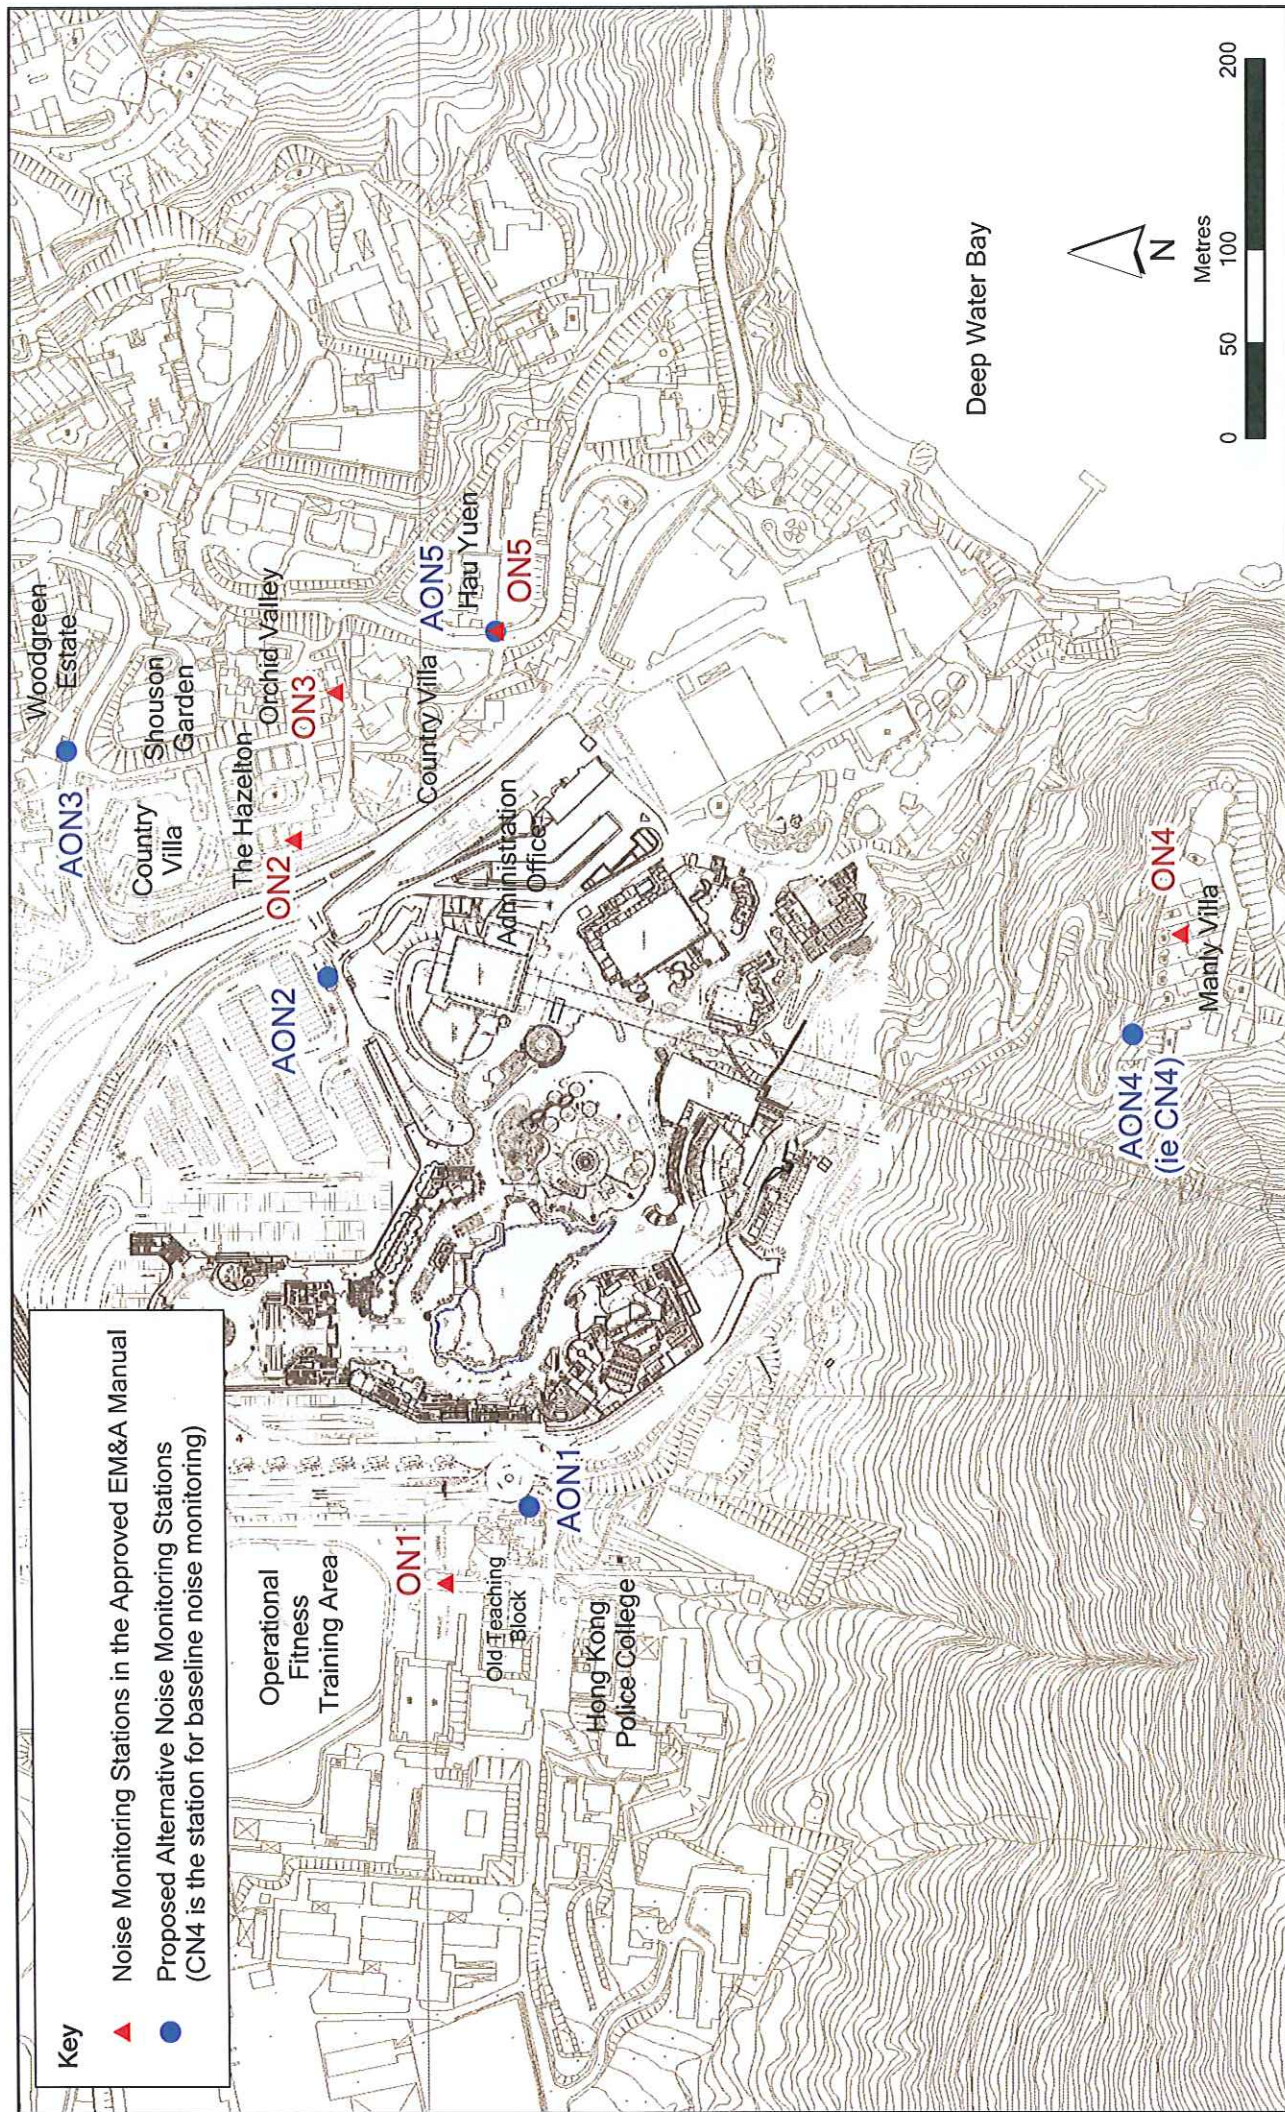


Figure 3.1

Proposed Noise Monitoring Stations in the Approved EM&A Manual and Proposed Alternative Noise Monitoring Stations

3.2.3

Monitoring Frequency

The monitoring for both lagoon night show noise monitoring and daily operational noise monitoring were conducted twice per week - one on a normal weekday and one on a general holiday, including Sundays during this reporting month.

3.2.4

Monitoring Methodology

The sound level meters and calibrator used for the noise monitoring, as listed in Table 3.2 below, complies with IEC 651: 1979 and 804:1985 (Type 1) specification.

Table 3.2 *Noise Measurement Equipments*

Monitoring Location		Monitoring Equipment
AON1	Open Area adjacent to Police Training School	RION NA-27 Sound Level Meter RION NC-73 calibrator
AON2	Old canteen building, Ocean Park	RION NL-31 Sound Level Meter RION NC-73 calibrator
AON3	Woodgreen Estate	RION NL-31 Sound Level Meter RION NC-73 calibrator
AON4	Manly Villa	RION NL-31 Sound Level Meter RION NC-73 calibrator
AON5	Hau Yuen	RION NL-31 Sound Level Meter RION NC-73 calibrator

Noise monitoring was conducted with reference to the calibration and measurement procedures as stated in the *Technical Memorandum for the Assessment of Noise from Places other than Domestic Premises, Public Places or Construction Sites (IND-TM)*. Immediately prior to and following each noise measurement the accuracy of the monitoring equipments was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements were accepted if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

The sound level meters and acoustic calibrator have been calibrated by a HOKLAS accredited laboratory every two years. The relevant calibration certificates are presented in *Annex B1*.

Noise measurements were made without the presence of fog and rain, and with steady wind speed and gusts not exceeding 5ms⁻¹ and 10 ms⁻¹, respectively in accordance with international standards and practices ⁽¹⁾. Broadband measurement of L_{Aeq}, L₁₀, L₉₀, L_{max} and L_{min} has been recorded at 100ms interval.

(1) ISO 11819-1:1997 and ISO/FDIS 13472-1:2001

3.2.5 Compliance Assessment

Fixed Plant Noise

As recommended in the EIA and stated in the EM&A Manual, OPC will follow the Action and Limit (A/L) Levels as recommended in EIA and EM&A Manual which are summarised in *Table 3.3*. In case exceedances are resulted from cumulative impacts, all steps stipulated in the Event/ Action Plan shall be followed.

Table 3.3 *Action and Limit Levels for Entertainment Noise*

Identification No.	Action Level	Limit Level
ON1/AON1	When documented complaint is received from any one of the sensitive receivers	L_{eq} (30 min) 60 dB(A)
ON2/AON2		L_{eq} (30 min) 60 dB(A)
ON3/AON3		L_{eq} (30 min) 55 dB(A)
ON4/AON4		L_{eq} (30 min) 55 dB(A)
ON5/AON5		L_{eq} (30 min) 55 dB(A)

3.3 RESULTS OF NOISE MONITORING

The measured noise levels at the monitoring locations are given in *Annex B2* and graphically presented in *Annex B3*.

Results indicated that the background corrected Lagoon Night Show Noise Levels has complied with the Limit Level at all monitoring stations during all monitoring dates.

The background corrected Noise Levels complied with the Limit Levels at most of the monitoring stations during most of the monitoring dates. Noise exceedances were recorded at AON1 (Open Area adjacent to Police Training School) due to high background noise from the visitors and traffic during public holidays and AON3 (Woodgreen Estate) and AON5 (Hau Yuen) due to the traffic noise from Shouson Hill Road.

Noise exceedance was also recorded at AON2 (Roof of Old Canteen Building) on 14 June 2011 due to the construction works near the Cable Car Terminal (CNP No. GW-RS0314-11) (See *Annex B4*).

Detail discussion on noise exceedances are given in *Section 3.4* below.

3.4 SUMMARY OF NOISE EXCEEDANCES

Noise exceedances recorded during this reporting period are summarised in *Table 3.4* below.

Table 3.4 *Summary of Daily Operational Noise Exceedance during this Reporting Period*

Date	Noise Monitoring Station	Measured Noise Level, dB(A)		Daily Operational Noise Level (Background Corrected) ^(a) , L_{eq} (30min) dB(A)	Limit Level, L_{eq} (30 min) dB(A)
		Daily Operational Noise Level, L_{eq} (30min) dB(A)	Background Noise Level, L_{eq} (15min) dB(A)		
29 May 2011 (Public Holiday)	AON1	67.6	65.1	67.0	60
	AON3	64.4	61.5	61.2	55
31 May 2011 (Weekday)	AON3	66.1	64.0	61.9	55
5 June 2011 (Public Holiday)	AON1	66.0	64.8	62.9	60
		65.7 (Lagoon Night Show Noise Level)	64.8	61.4 (Lagoon Night Show Noise Level (Background corrected))	60
	AON3	64.2	61.9	60.3	55
7 June 2011 (Weekday)	AON3	62.7	61.2	57.4	55
12 June 2011 (Public Holiday)	AON1	66.9	65.8	63.5	60
14 June 2011 (Weekday)	AON2	68.8 (Lagoon Night Show Noise Level)	67.1	63.7 (Lagoon Night Show Noise Level (Background corrected))	60
	AON5	59.0	55.8	56.1	55
19 June 2011 (Public Holiday)	AON1	65.4	64.5	61.1	60
21 June 2011 (Weekday)	AON3	66.3	64.9	60.5	55
	AON5	59.0	55.3	56.6	55

Note:
 (a) The Background Corrected Noise Levels were either measured in front of a façade at AON2, AON3, AON4 and AON5 or with façade correction of 3 dB(A) at AON1.

AON1 – High Background Noise during Public Holidays

The monitoring station AON1 is directly facing the bus terminus of the Ocean Park. The measured noise levels were dominated by the bus movements, ie. bus moving in and out of the terminus to pick up visitors leaving the Ocean Park during evening time. The measured background noise levels were in the range of 62 to 66 dB(A), ie 2 to 6 dB(A) higher than the Limit Level, during the four days with noise exceedances as they were public holidays/ Sundays with more visitors (see Table 3.4).

AON3 and AON5 – Traffic Noise from Shouson Hill Road

The exceedances at AON3 and AON5 were mainly due to the traffic at Shouson Hill Road.

Summary

As mentioned above, the noise exceedances were due to the bus movements at the bus terminus during public holidays and traffic from Shouson Hill Road, ie not due to the fixed plant noise sources or the lagoon night show from the Ocean Park.

The Open-air Night Show commenced on 27 January 2011. According to the requirements set out in the Environmental Permit (EP) and the updated EM&A Manual, air quality and noise monitoring shall be carried out during the first year of the operation of Open-air Night Show. This is the 5th air quality and noise monitoring report which summarises the impact monitoring results during the reporting period from 27 May to 26 June 2011.

24-hr average respirable suspended particulates (RSP) monitoring were conducted at three designated monitoring stations, one on the rooftop of the Administrative Building in OP (AM1), one on the Landscape Storage Area in Ocean Park (AM2) and one on the Rooftop of Main Medical Block of Graham Hospital (AM3) on 16 June 2011. All monitored 24-hour average RSP concentrations measured at AM1, AM2 and AM3 complied with the Action/Limit (A/L) Level. Since the measured 24-hr average RSP concentrations at AM2 and AM3 complied with A/L Level, the monitoring frequency will be reduced to monthly in the next month.

Daily operational noise and lagoon night show noise monitoring were carried out at five designated monitoring stations during this reporting period. Out of the 5 stations, noise exceedances were recorded at AON1 (Open Area adjacent to Police Training School), AON3 (Orchid Valley) and AON5 (Hau Yuen) due to noise emanating from the bus terminus, high background noise from visitors and traffic during the public holidays, and the traffic noise from Shouson Hill Road.

Annex A1

HVS Calibration Report



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MS WINNIE KO
CLIENT: ERM HONG KONG
ADDRESS: 21/F, LINCOLN HOUSE, 979 KING`S ROAD,
TAIKOO PLACE, ISLAND EAST,
QUARRY BAY, HONG KONG.
PROJECT: OPC AIR QUALITY MONITORING FOR OPERATION
OF SYMBIO SHOW

WORK ORDER: HK1107184
LABORATORY: HONG KONG
DATE RECEIVED: 24/03/2011
DATE OF ISSUE: 04/04/2011
SAMPLE TYPE: EQUIPMENT
No. of SAMPLES: 3

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of ALS will be followed.

Scope of Test: Flow Rate
Description: High Volume Sampler
Brand Name: TISCH
Model No.: --
Serial No.: --
Equipment No.: HK647, HK649, HK651
Date of Calibration: 24 March, 2011

NOTES


This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd
11/F Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung
HONG KONG

Phone: 852-2610 1044
Fax: 852-2610 2021
Email: hongkong@alsglobal.com


Mr Chan Kwok Fai, Godfrey
Laboratory Manager - Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

ADDRESS 11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong PHONE +852 2610 1044 FAX +852 2610 2021
ALS TECHNICHEM (HK) PTY LTD Part of the ALS Laboratory Group A Campbell Brothers Limited Company



Calibration Report for High Volume Sampler (RSP Sampler)

Report No. : HK1107184
Location : (AM1)
Brand Name : TISCH

Equipment No. : HK649
Calibration date : 24/03/2011
Calibration Due date : 24/06/2011

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition					
Ambient			Seasonal		
Temperature, Ta	291.5	K	Temperature, Ts	291.3	K
Pressure, Pa	1016	hPa	Pressure, Ps	1018	hPa
Orifice Transfer Standards Information					
Equipment No.	TE-5025A (#1483)	Slope, m_c	1.25411	Intercept, b_c	-0.00314
Last Calibration Date	02-June-2010	$Q_a = [\sqrt{(\Delta H \cdot Ta / Pa) - b_c}] / m_c$			
Next Calibration Date	02-June-2011				

Calibration of RSP				
Calibration Point	Manometer Reading H(inches of water) (ΔH)	Q_{std} (m^3/min) X-axis	Continuous Flow Recorder, W (CFM)	$W((Ta+30)/Pa)^{1/2}$ Y-axis
1	13.0	1.5425	55	30.9390
2	10.4	1.3799	49	27.5638
3	8.6	1.2550	44	24.7512
4	5.3	0.9858	34	19.1259
5	3.6	0.8129	27	15.1882

By Linear Regression of Y Vs X

Correlation coefficient, R = 0.9999
Slope, m = 21.5400
Intercept, b = -2.2311
Calibration result :

*If the correlation coefficient, R is < 0.9900. Checking and recalibration are required.

Remarks :

Calibration by : Sam Wong
Signature : Sam Wong
Date : 24/03/2011

Checked by : Iris Lin
Signature : Iris Lin
Date : 31/03/2011

ALS Technichem (HK) Pty Ltd.



Calibration Report for High Volume Sampler (RSP Sampler)

Work Order No. : HK1107184
 Location : (AM2)
 Brand Name : TISCH

ALS Equipment No. : HK647
 Calibration date : 24/03/2011
 Calibration Due date : 24/06/2011

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition					
Ambient			Seasonal		
Temperature, Ta	291.9	K	Temperature, Ts	291.3	K
Pressure, Pa	1016	hPa	Pressure, Ps	1018	hPa
Orifice Transfer Standards Information					
Equipment No.	TE-5025A (#1483)	Slope, m_c	1.25411	Intercept, b_c	-0.00314
Last Calibration Date	02-June-2010	$Q_a = [\sqrt{(\Delta H \cdot T_a / Pa) - b_c}] / m_c$			
Next Calibration Date	02-June-2011				

Calibration of RSP				
Calibration Point	Manometer Reading H(inches of water) (ΔH)	Q_{std} (m^3/min) X-axis	Continuous Flow Recorder, W (CFM) Y-axis	$W((T_a + 30)/Pa)^{1/2}$ Y-axis
1	12.0	1.4831	55	30.9582
2	9.2	1.2989	47	26.4552
3	7.9	1.2038	44	24.7666
4	4.8	0.9389	32	18.0121
5	3.5	0.8021	25	14.0719

By Linear Regression of Y Vs X

Correlation coefficient, R = 0.9987
 Slope, m = 24.5974
 Intercept, b = -5.3196
 Calibration result :

*If the correlation coefficient, R is < 0.9900. Checking and recalibration are required.

Remarks :

Calibration by : Sam Wong
 Signature : Sam Wong
 Date : 24/03/2011

Checked by : Iris Lin
 Signature : Iris Lin
 Date : 31/03/2011



Calibration Report for High Volume Sampler (RSP Sampler)

Report No. : HK1107184
 Location : (AM3)
 TISCH

Equipment No. : HK651
 Calibration date : 24/03/2011
 Calibration Due date : 24/06/2011

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition					
Ambient			Seasonal		
Temperature, Ta	292.1	K	Temperature, Ts	291.3	K
Pressure, Pa	1016	hPa	Pressure, Ps	1018	hPa
Orifice Transfer Standards Information					
Equipment No.	TE-5025A (#1483)	Slope, m_c	1.25411	Intercept, b_c	-0.00314
Last Calibration Date	02-June-2010	$Q_a = [\sqrt{(\Delta H \cdot Ta/Pa) - b_c}] / m_c$			
Next Calibration Date	02-June-2011				

Calibration of RSP				
Calibration Point	Manometer Reading H(inches of water) (ΔH)	Q_{std} (m^3/min) X-axis	Continuous Flow Recorder, W (CFM)	$W((Ta+30)/Pa)^{1/2}$ Y-axis
1	13.3	1.5617	61	34.3462
2	10.3	1.3747	53	29.8418
3	8.8	1.2708	50	28.1526
4	5.0	0.9585	39	21.9590
5	3.8	0.8359	32	18.0177

By Linear Regression of Y Vs X

Correlation coefficient, R = 0.9969
 Slope, m = 21.6216
 Intercept, b = 0.5103
 Calibration result :

*If the correlation coefficient, R is < 0.9900. Checking and recalibration are required.

Remarks :

Calibration by : Sam Wong
 Signature : Sam Wong
 Date : 24/03/2011


Checked by : Iris Lin
 Signature : Iris Lin
 Date : 31/03/2011

Annex A2

Laboratory Report

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group ANALYTICAL CHEMISTRY & TESTING SERVICES



CERTIFICATE OF ANALYSIS

Client	: ERM HONG KONG	Laboratory	: ALS Technichem HK Pty Ltd	Page	: 1 of 2
Contact	: MS CELINE LEE	Contact	: Chan Kwok Fai, Godfrey	Work Order	: HK1113893
Address	: 21/F, LINCOLN HOUSE, 979 KING'S ROAD, TAIKOO PLACE, ISLAND EAST, QUARRY BAY, HONG KONG	Address	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	: Celine.Lee@erm.com	E-mail	: Godfrey.Chan@alsenviro.com		
Telephone	: +852 2271 3000	Telephone	: +852 2610 1044		
Facsimile	: +852 2723 5660	Facsimile	: +852 2610 2021		
Project	: OPC AIR QUALITY MONITORING FOR OPERATION OF SYMBIO SHOW	Quote number	: ---	Date Samples Received	: 20-JUN-2011
Order number	: ---			Issue Date	: 23-JUN-2011
C-O-C number	: ---			No. of samples received	: 3
Site	: OCEAN PARK			No. of samples analysed	: 3

General Comments

This report supersedes any previous report(s) with this reference. Results apply to the sample(s) as submitted. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. The completion date of analysis is:

23-JUN-2011

Key: LOR = Limit of reporting: CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.
Specific comments for Work Order: HK1113893

Sample(s) were collected by ALS Technichem (HK) staff on 20 June, 2011.
Sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the Electronic Transactions Ordinance of Hong Kong, Chapter 553, Section 6.

Signatories	Position	Authorised results for
Fung Lim Chee, Richard	General Manager	Inorganics

ALS Laboratory Group
Trading Name: ALS Technichem (HK) Pty Ltd
11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com
A Campbell Brothers Limited Company



Analytical Results

Sub-Matrix: FILTER

Analytical Results					
Sub-Matrix: FILTER					
Compound	Client sample ID				
	CAS Number	LOR	Unit		
EAI/ED: Physical and Aggregate Properties					
HK-RSP: Respirable Suspended Particulate	---	0.01	mg/m³	0.03	0.02

Annex A3

Detailed Summary and Graphical Presentation of the Cumulative Results since Commencement of Open-air Night Show

Annex A3 Measured 24-hour Average RSP Concentrations

RSP Monitoring Station : AM1 (Rooftop of Administration Building in Ocean Park)

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m ³ /min)			RSP Conc. (µg/m ³)	Limit Level (µg/m ³)	Filter ID
										Initial	Final	Average			
28-Jan-11	17:00	29-Jan-11	17:00	Sunny	2.8652	2.9914	17711.68	17735.95	24.27	1.39	1.39	1.39	63	180	202102
04-Feb-11	17:00	05-Feb-11	17:00	Sunny	2.8755	3.0567	17735.95	17760.30	24.35	1.39	1.43	1.41	88	180	202099
12-Feb-11	17:00	13-Feb-11	17:00	Cloudy	2.8808	3.0820	17760.30	17784.33	24.03	1.39	1.39	1.39	101	180	202100
20-Feb-11	17:00	21-Feb-11	17:00	Cloudy	2.8770	2.9497	17784.33	17808.45	24.12	1.39	1.39	1.39	36	180	202101
22-Mar-11	17:00	23-Mar-11	17:00	Cloudy	2.7967	2.8948	17808.45	17833.61	25.16	1.49	1.49	1.49	44	180	202264
10-Apr-11	17:00	11-Apr-11	17:00	Cloudy	2.7924	2.9167	17842.11	17866.14	24.03	1.08	1.08	1.08	80	180	202288
11-May-11	17:00	12-May-11	17:00	Sunny	2.7992	2.8443	17866.14	17890.29	24.15	1.04	1.04	1.04	30	180	202567
16-Jun-11	17:00	17-Jun-11	17:00	Sunny	2.7956	2.8404	17890.39	17914.31	23.92	1.14	1.14	1.14	27	180	202570
										Min.			27		
										Max.			101		
										Average			59		

Annex A3
Measured 24-hour Average RSP Concentrations

RSP Monitoring Station : AM2 (Landscape Storage Area in Ocean Park)


Start Date	Time	Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m ³ /min)		RSP Conc. (µg/m ³)	Limit Level (µg/m ³)	Filter ID
		Date	Time		Initial	Final	Initial	Final		Initial	Final			
28-Mar-11	17:00	29-Mar-11	17:00	Cloudy	2.7923	2.8849	5069.23	5092.98	23.75	1.04	1.04	62	180	202287
04-Apr-11	17:00	05-Apr-11	17:00	Cloudy	2.7884	2.9238	5092.98	5116.98	24.00	1.47	1.47	64	180	202290
10-Apr-11	17:00	11-Apr-11	17:00	Cloudy	2.7727	2.8799	5116.98	5140.98	24.00	1.45	1.45	51	180	202291
18-Apr-11	17:00	19-Apr-11	17:00	Sunny	2.8004	2.9833	5140.98	5164.98	24.00	1.43	1.43	89	180	202292
11-May-11	17:00	12-May-11	17:00	Sunny	2.8064	2.8596	5164.98	5188.98	24.00	1.43	1.43	26	180	202568
16-Jun-11	17:00	17-Jun-11	17:00	Sunny	2.7984	2.8285	5189.07	5213.07	24.00	1.19	1.19	18	180	202571
										Min.		18		
										Max.		89		
										Average		52		

Measured 24-hour Average RSP Concentrations


AM3 (Rooftop of Main Medical Block of Graham Hospital)

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m³/min)			RSP Conc. (µg/m³)	Limit Level (µg/m³)	Filter ID
		Date	Time		Initial	Final	Initial	Final		Initial	Final	Average			
28-Mar-11	17:00	29-Mar-11	17:00	Cloudy	2.7946	2.9435	13068.67	13092.67	24.00	0.91	0.91	0.91	114	180	202265
04-Apr-11	17:00	05-Apr-11	17:00	Cloudy	2.8005	2.9049	13092.67	13116.68	24.01	0.65	0.65	0.65	112	180	202289
10-Apr-11	17:00	11-Apr-11	17:00	Sunny	2.7948	2.8825	13116.68	13140.66	23.98	0.70	0.70	0.70	87	180	202294
18-Apr-11	17:00	19-Apr-11	17:00	Sunny	2.7966	2.9578	13140.66	13164.68	24.02	0.70	0.70	0.70	160	180	202295
11-May-11	17:00	12-May-11	17:00	Sunny	2.7906	2.8330	13164.68	13188.69	24.01	0.74	0.74	0.74	40	180	202566
16-Jun-11	17:00	17-Jun-11	17:00	Sunny	2.8008	2.8294	13188.72	13212.72	24.00	1.08	1.08	1.08	18	180	202569
											Min.	18			
											Max.	160			
											Average	88			


Measured 24-hr Average RSP Concentration AM1 - Rooftop of Administrative Building (Former Staff Quarters) in Ocean Park

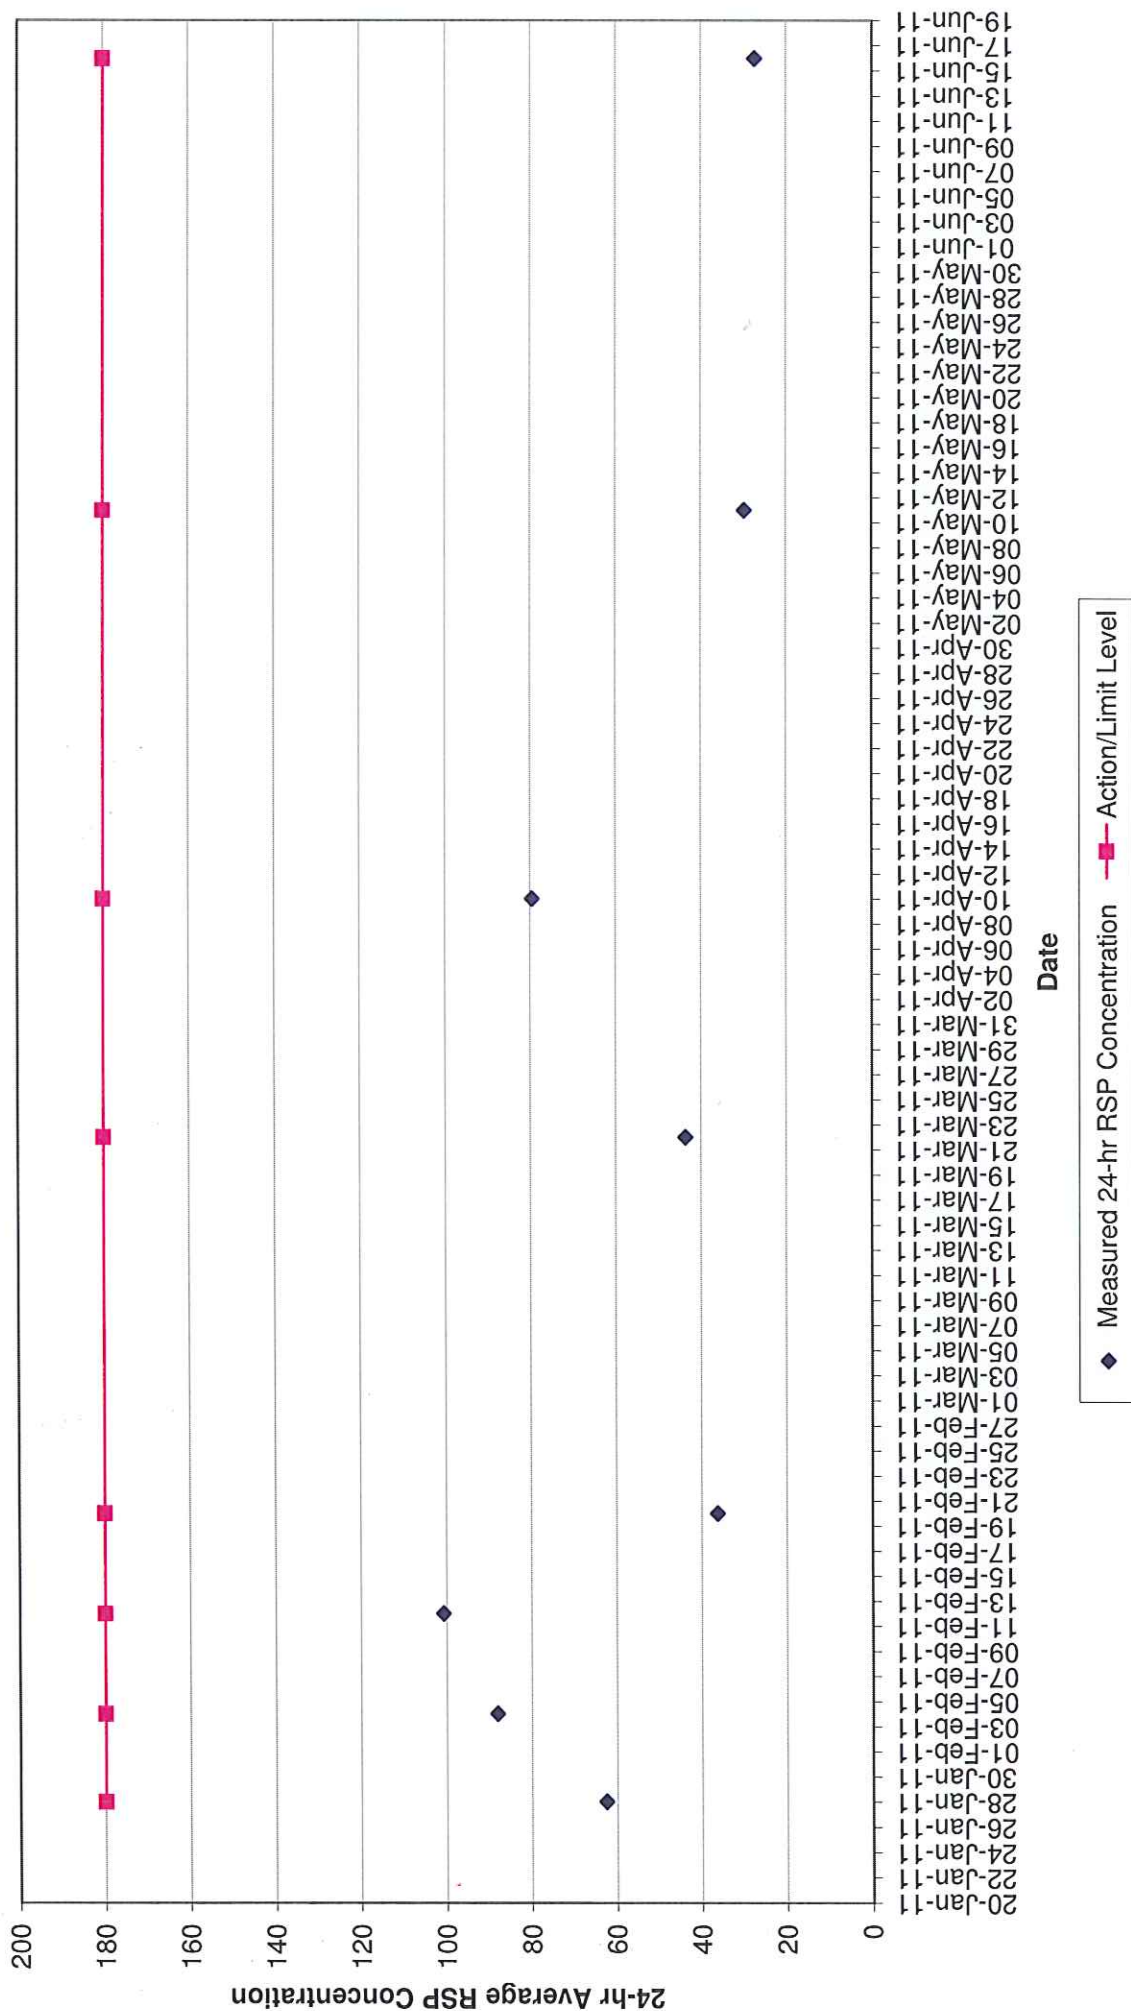

Measured 24-hr Average RSP Concentration
AM 2 - Landscape Storage Area in Ocean Park

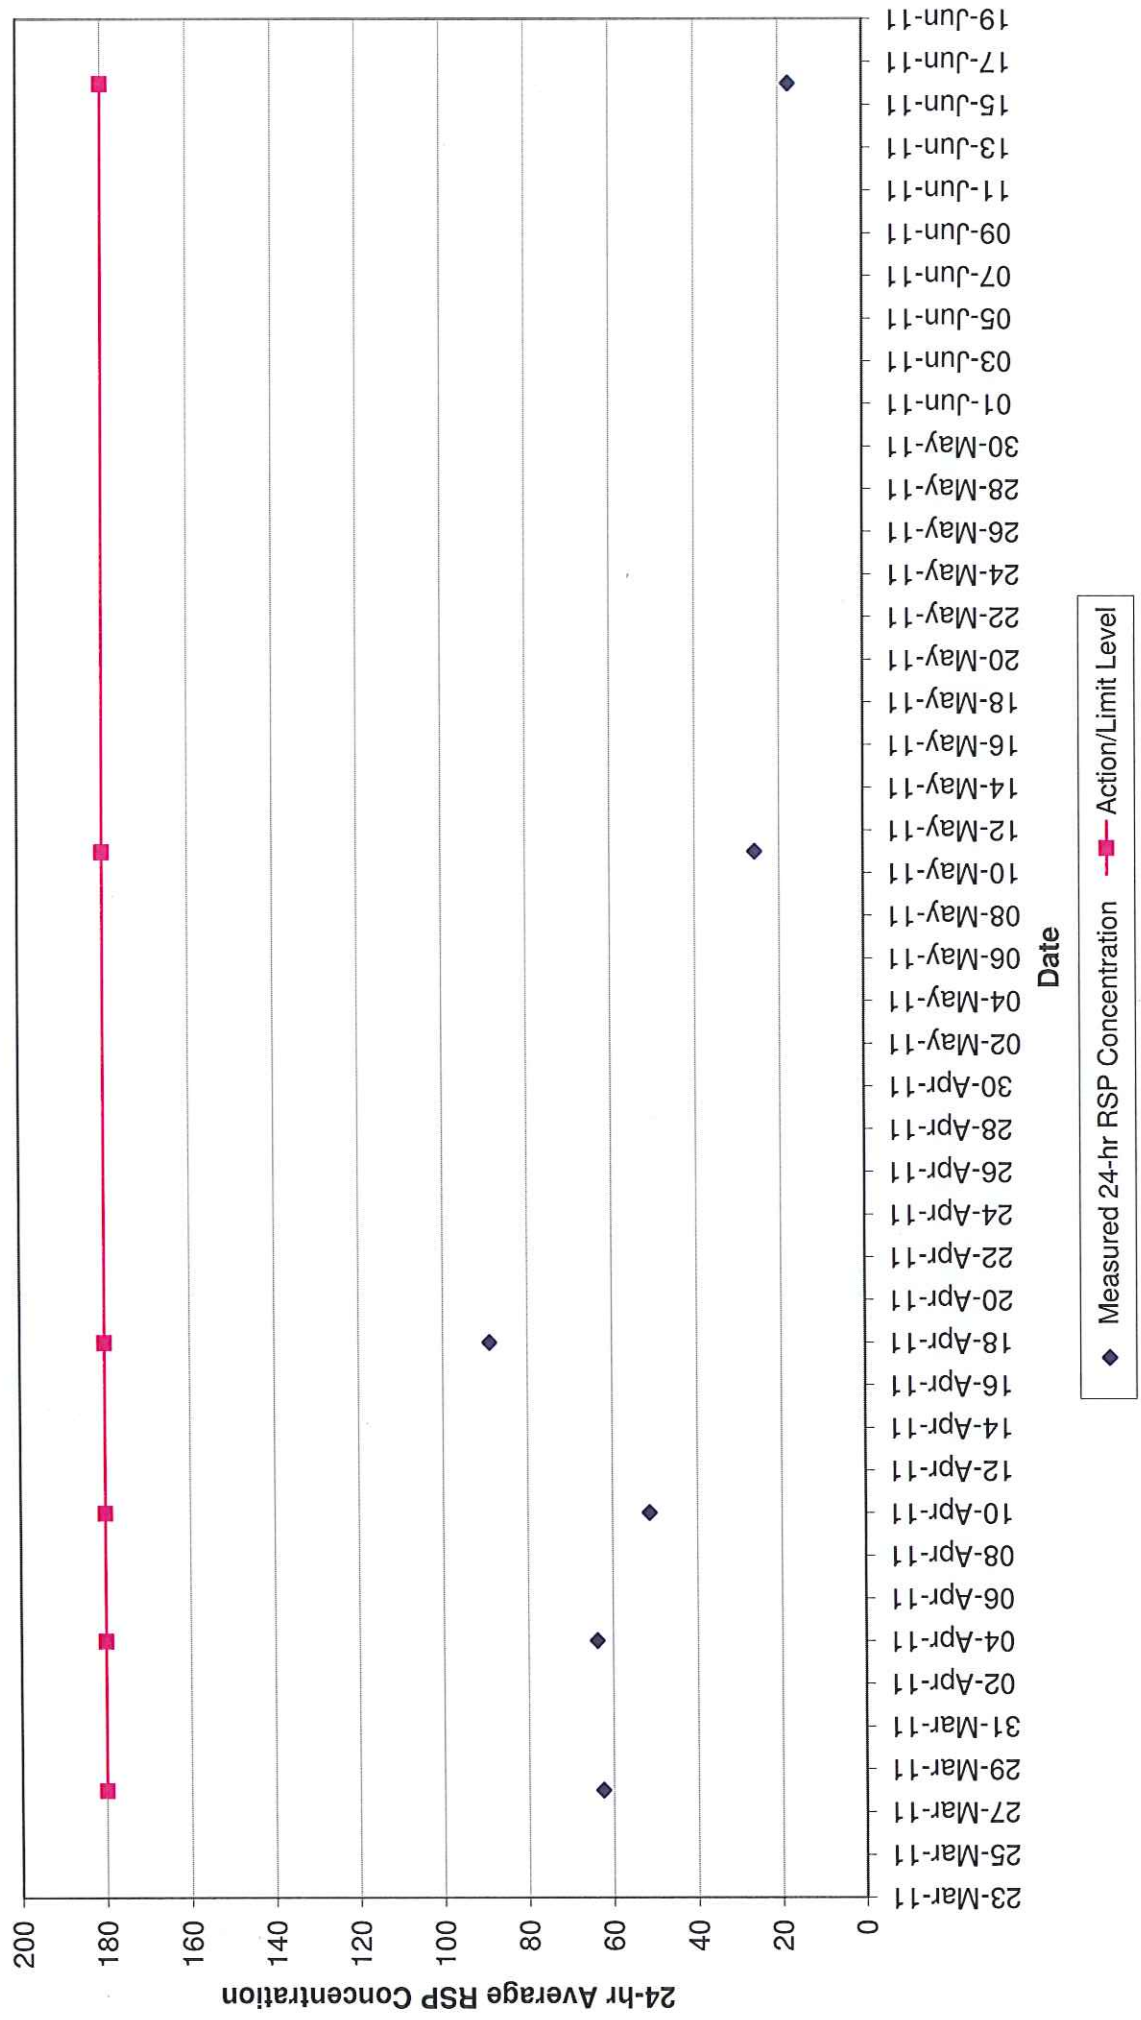

Measured 24-hr Average RSP Concentration AM3 - Rooftop of Main Medical Block of Graham Hospital

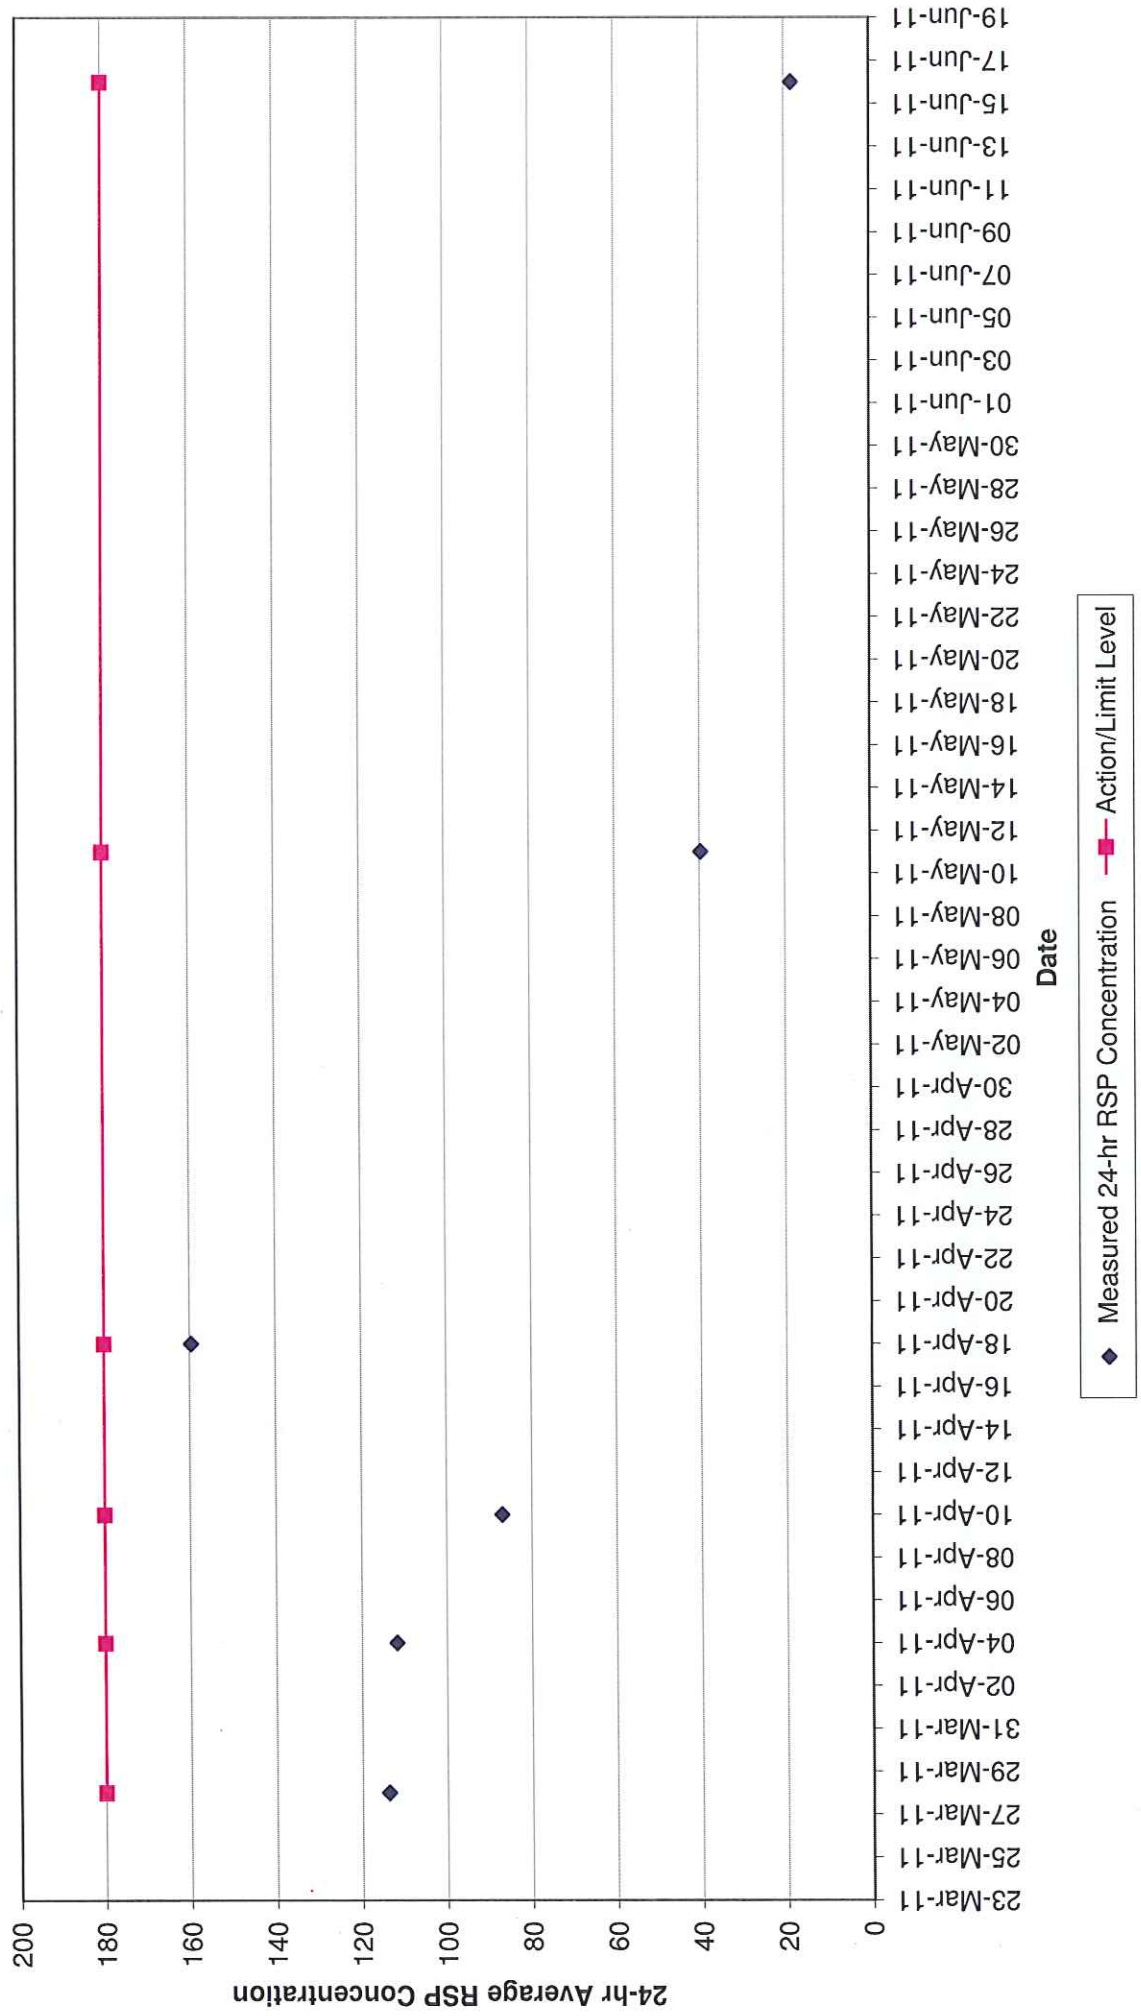

Annex A4

Recorded RSP
Concentrations at EPD's
AQMSs in Tung Chung,
Shatin, Tai Po, Yuen Long
and Tap Mun on ***16 June
2011***

Recorded RSP Concentrations at EPD's AQMSs in Tung Chung, Shatin, Tai Po, Yuen Long, and Tap Mun on 16 June 2011

16 June 2011

Tung Chung

Date & Time	RSP
17-06-2011 16:00	12.6
17-06-2011 15:00	12.3
17-06-2011 14:00	8.7
17-06-2011 13:00	8.1
17-06-2011 12:00	6.5
17-06-2011 11:00	10.6
17-06-2011 10:00	5.1
17-06-2011 9:00	7
17-06-2011 8:00	4.7
17-06-2011 7:00	5.7
17-06-2011 6:00	2.2
17-06-2011 5:00	6.1
17-06-2011 4:00	4.2
17-06-2011 3:00	8.8
17-06-2011 2:00	8.7
17-06-2011 1:00	9
17-06-2011 0:00	10.2
16-06-2011 23:00	9.6
16-06-2011 22:00	12.5
16-06-2011 21:00	12.7
16-06-2011 20:00	14.8
16-06-2011 19:00	9.3
16-06-2011 18:00	5.3
16-06-2011 17:00	13.3

Shatin

Date & Time	RSP
17-06-2011 16:00	22.6
17-06-2011 15:00	18.5
17-06-2011 14:00	13.5
17-06-2011 13:00	19.4
17-06-2011 12:00	14.5
17-06-2011 11:00	28.6
17-06-2011 10:00	16.7
17-06-2011 9:00	17.3
17-06-2011 8:00	9.7
17-06-2011 7:00	12.1
17-06-2011 6:00	10
17-06-2011 5:00	9.5
17-06-2011 4:00	5.1
17-06-2011 3:00	7.5
17-06-2011 2:00	9.2
17-06-2011 1:00	11.3
17-06-2011 0:00	12.2
16-06-2011 23:00	21.1
16-06-2011 22:00	16.4
16-06-2011 21:00	14.6
16-06-2011 20:00	11.4
16-06-2011 19:00	13.5
16-06-2011 18:00	14.5
16-06-2011 17:00	8.5

Tai Po

Date & Time	RSP
17-06-2011 16:00	16.1
17-06-2011 15:00	12.7
17-06-2011 14:00	14
17-06-2011 13:00	10.1
17-06-2011 12:00	12.8
17-06-2011 11:00	17.1
17-06-2011 10:00	15.2
17-06-2011 9:00	19.2
17-06-2011 8:00	14.9
17-06-2011 7:00	11.5
17-06-2011 6:00	10.8
17-06-2011 5:00	8.8
17-06-2011 4:00	5.4
17-06-2011 3:00	8
17-06-2011 2:00	10.4
17-06-2011 1:00	10.7
17-06-2011 0:00	11.6
16-06-2011 23:00	10.4
16-06-2011 22:00	13.2
16-06-2011 21:00	16.3
16-06-2011 20:00	15.1
16-06-2011 19:00	13.5
16-06-2011 18:00	13.3
16-06-2011 17:00	5.7

Yuen Long

Date & Time	RSP
17-06-2011 16:00	19.4
17-06-2011 15:00	17.1
17-06-2011 14:00	17.2
17-06-2011 13:00	17.5
17-06-2011 12:00	14.6
17-06-2011 11:00	14
17-06-2011 10:00	15.2
17-06-2011 9:00	14
17-06-2011 8:00	18.1
17-06-2011 7:00	16.4
17-06-2011 6:00	9.7
17-06-2011 5:00	5.2
17-06-2011 4:00	6.9
17-06-2011 3:00	6.9
17-06-2011 2:00	10.4
17-06-2011 1:00	14.3
17-06-2011 0:00	18.4
16-06-2011 23:00	18.9
16-06-2011 22:00	19.6
16-06-2011 21:00	22.4
16-06-2011 20:00	19.4
16-06-2011 19:00	16
16-06-2011 18:00	8.7
16-06-2011 17:00	14.5

Tap Mun



Date & Time	RSP
17-06-2011 16:00	29.9
17-06-2011 15:00	21.5
17-06-2011 14:00	19.1
17-06-2011 13:00	17
17-06-2011 12:00	14.6
17-06-2011 11:00	12.9
17-06-2011 10:00	10.7
17-06-2011 9:00	12.1
17-06-2011 8:00	18.2
17-06-2011 7:00	12.1
17-06-2011 6:00	22.8
17-06-2011 5:00	31.9
17-06-2011 4:00	18
17-06-2011 3:00	23.7
17-06-2011 2:00	20.7
17-06-2011 1:00	15.6
17-06-2011 0:00	15.7
16-06-2011 23:00	13.8
16-06-2011 22:00	13.3
16-06-2011 21:00	9.7
16-06-2011 20:00	10.3
16-06-2011 19:00	9
16-06-2011 18:00	11.4
16-06-2011 17:00	8

Annex A5


Weather Data Recorded at
HKO's Weather Station in
Wong Chuk Hang on **16**
June 2011


16 June 2011

Prevailing Wind Speed

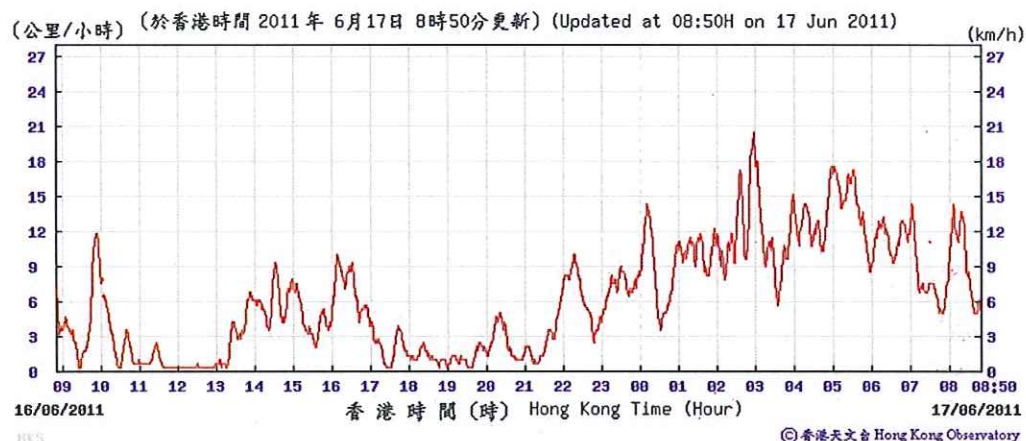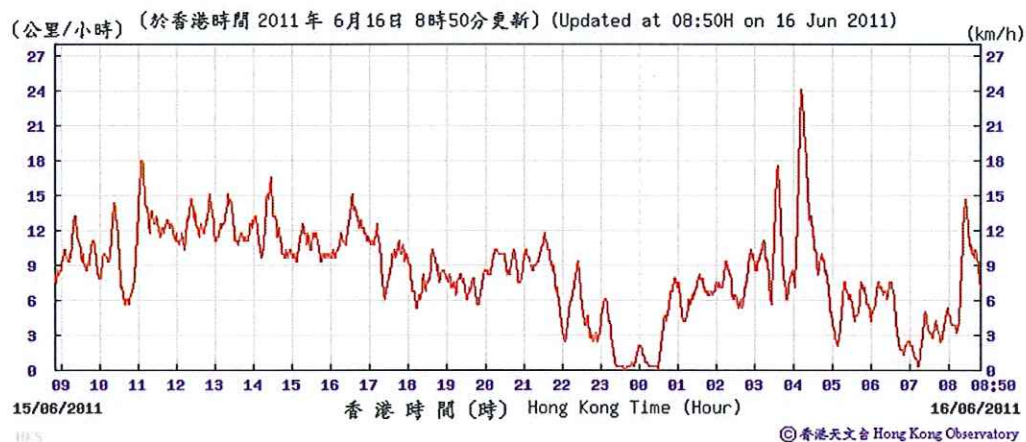


Prevailing Wind Direction

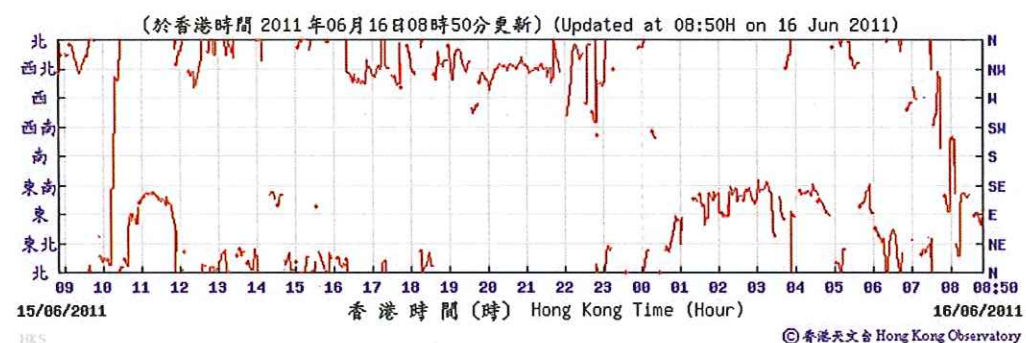

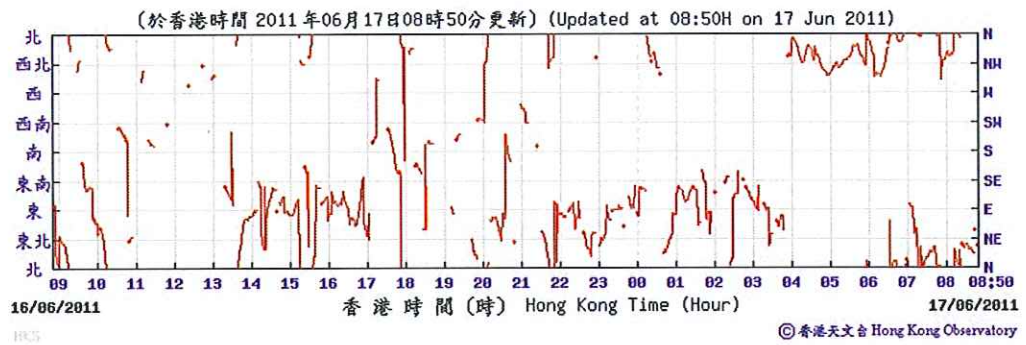

Ambient Temperature and Relative Humidity

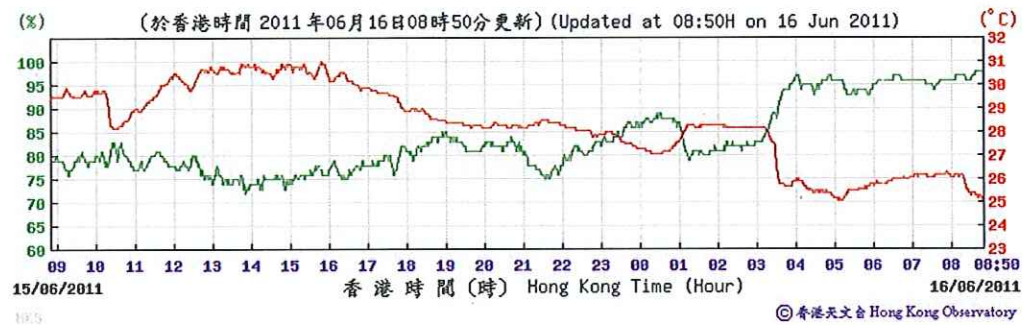

Annex B1

Calibration Certificates of the Noise Measurement Equipment



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C103766

Certificate of Calibration

This is to certify that the equipment

Description : Sound Level Calibrator

Manufacturer : Rion

Model No. : NC-73

Serial No. : 10786708

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C103766.*

The equipment is supplied by

Co. Name : Envirotech Services Co.

*Address : Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,
Hong Kong*

Date of Issue : 13 July 2010

Certified by :

K.C. Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C103766

Calibration Report

ITEM TESTED

DESCRIPTION : Sound Level Calibrator
MANUFACTURER : Rion
MODEL NO. : NC-73
SERIAL NO. : 10786708

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 12 July 2010

JOB NO. : IC10-1738

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested by :


L L Cheung

Date : 13 July 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 2

Report No. : C103766

Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours before the commencement of the test.
2. The results presented are the mean of 3 measurements at each calibration point.
3. Test equipment :

Equipment ID	Description	Certificate No.
TST150A	Measuring Amplifier	C101008
CL130	Universal Counter	C103289
CL281	Multifunction Acoustic Calibrator	C1005490

4. Test procedure : MA100N.

5. Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.991 0	1 kHz ± 2 %	± 0.1

Remark : - The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C103852

Certificate of Calibration

This is to certify that the equipment

Description : Precision Sound Level Meter

Manufacturer : Rion

Model No. : NA-27

Serial No. : 00201194

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C103852.*

The equipment is supplied by

Co. Name : Envirotech Services Co.

*Address : Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,
Hong Kong*

Date of Issue : 15 July 2010

Certified by :

K.C. Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C103852

Calibration Report

ITEM TESTED

DESCRIPTION : Precision Sound Level Meter
MANUFACTURER : Rion
MODEL NO. : NA-27
SERIAL NO. : 00201194

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$
LINE VOLTAGE : ---

RELATIVE HUMIDITY : $(55 \pm 20)\%$

TEST SPECIFICATIONS

Calibration

DATE OF TEST : 15 July 2010

JOB NO. : IC10-1790

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested by :


L L Cheung

Date : 15 July 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 4



Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration using the internal standard (After Adjustment) was performed before the test 6.1.2 - 6.4.
3. The results presented are the mean of 3 measurement at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C100067
CL281	Multifunction Acoustic Calibrator	DC1005490

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting			Applied Value		UUT Reading (dB)		IEC 60651 Type 1 Spec. (dB)
Range (dB)	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Before Adjustment	After Adjustment	
50 - 110	LA	Fast	94.00	1	94.6	94.0	± 0.7

- 6.1.2 Linearity

UUT Setting			Applied Value		UUT Reading (dB)	
Range (dB)	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
60 - 120	LA	Fast	94.00	1	94.0	(Ref.)
			104.00		104.0	
			114.00		114.0	

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

- 6.2 Time Weighting

UUT Setting			Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 110	LA	Fast	94.00	1	94.0	Ref.
		Slow			94.0	± 0.1

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting			Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 110	LA	Fast	94.00	31.5 Hz	54.4	-39.4 ± 1.5
				63 Hz	67.7	-26.2 ± 1.5
				125 Hz	77.8	-16.1 ± 1.0
				250 Hz	85.2	-8.6 ± 1.0
				500 Hz	90.7	-3.2 ± 1.0
				1 kHz	94.0	Ref.
				2 kHz	95.2	+1.2 ± 1.0
				4 kHz	95.0	+1.0 ± 1.0
				8 kHz	92.8	-1.1 (+1.5 ; -3.0)
				12.5 kHz	89.7	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting			Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 110	LC	Fast	94.00	31.5 Hz	90.9	-3.0 ± 1.5
				63 Hz	93.1	-0.8 ± 1.5
				125 Hz	93.8	-0.2 ± 1.0
				250 Hz	93.9	0.0 ± 1.0
				500 Hz	94.0	0.0 ± 1.0
				1 kHz	93.9	Ref.
				2 kHz	93.8	-0.2 ± 1.0
				4 kHz	93.1	-0.8 ± 1.0
				8 kHz	90.9	-3.0 (+1.5 ; -3.0)
				12.5 kHz	87.7	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.4 Time Averaging

UUT Setting			Applied Value					UUT	IEC 60804
Range (dB)	Mode	Integrating Time	Freq. (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
50 - 110	LAeq	10 sec.	4	1	1/10	110.0	100	99.9	± 0.5
					1/10 ²		90	90.2	± 0.5
		60 sec.			1/10 ³		80	80.0	± 1.0
		5 min.			1/10 ⁴		70	70.0	± 1.0

Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value : 94 dB : 31.5 Hz - 125 Hz : ± 0.35 dB
250 Hz - 500 Hz : ± 0.30 dB
1 kHz : ± 0.20 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
12.5 kHz : ± 0.70 dB
104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C102904

Certificate of Calibration

This is to certify that the equipment

Description : Sound Level Meter

Manufacturer : Rion

Model No. : NL-31

Serial No. : 00410224

has been calibrated for the specific items and ranges.

The results are shown in the Calibration Report No. C102904.

The equipment is supplied by

Co. Name : Envirotech Services Co.

*Address : Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,
Hong Kong*

Date of Issue : 31 May 2010

Certified by :

K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F. Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C102904

Calibration Report

ITEM TESTED

DESCRIPTION : Sound Level Meter
MANUFACTURER : Rion
MODEL NO. : NL-31
SERIAL NO. : 00410224

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$
LINE VOLTAGE : ---

RELATIVE HUMIDITY : $(55 \pm 20)\%$

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 31 May 2010

JOB NO. : IC10-1356

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


L L Cheung

Date : 31 May 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 4



Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C100067
CL179	Acoustical Calibrator	C095223

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	93.9	± 0.7

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L _A	A	Fast	94.00	1	93.9 (Ref.)
				114.00		113.9

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

6.2 Time Weighting

6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	93.9	Ref.
			Slow			93.8	± 0.1

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _A	A	Fast	94.00	31.5 Hz	54.2	-39.4 ± 1.5
					63 Hz	67.6	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.0
					250 Hz	85.2	-8.6 ± 1.0
					500 Hz	90.6	-3.2 ± 1.0
					1 kHz	93.9	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.9	-1.1 (+1.5 ; -3.0)
					12.5 kHz	90.0	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _C	C	Fast	94.00	31.5 Hz	90.6	-3.0 ± 1.5
					63 Hz	93.1	-0.8 ± 1.5
					125 Hz	93.7	-0.2 ± 1.0
					250 Hz	93.9	0.0 ± 1.0
					500 Hz	93.9	0.0 ± 1.0
					1 kHz	93.9	Ref.
					2 kHz	93.9	-0.2 ± 1.0
					4 kHz	93.3	-0.8 ± 1.0
					8 kHz	91.0	-3.0 (+1.5 ; -3.0)
					12.5 kHz	88.1	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.4 Time Averaging

UUT Setting				Applied Value					UUT	IEC 60804
Range (dB)	Mode	Frequency Weighting	Time Weighting	Freq. (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
20 - 110	L _{Aeq}	A	10 sec.	4	1	1/10	110.0	100	100.0	± 0.5
			1/10 ²			90		90.0	± 0.5	
			1/10 ³			80		80.0	± 1.0	
			1/10 ⁴			70		70.0	± 1.0	

Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value : 94 dB : 31.5 Hz - 125 Hz : ± 0.35 dB
250 Hz - 1 kHz : ± 0.30 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
12.5 kHz : ± 0.70 dB
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C103778

Certificate of Calibration

This is to certify that the equipment

Description : Sound Level Meter

Manufacturer : Rion

Model No. : NL-31

Serial No. : 00320533

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C103778.*

The equipment is supplied by

Co. Name : Envirotech Services Co.

*Address : Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,
Hong Kong*

Date of Issue : 13 July 2010

Certified by :

K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C103778

Calibration Report

ITEM TESTED

DESCRIPTION : Sound Level Meter
MANUFACTURER : Rion
MODEL NO. : NL-31
SERIAL NO. : 00320533

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 12 July 2010

JOB NO. : IC10-1738

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested by :


L L Cheung

Date : 13 July 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 4

Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C100067
CL281	Multifunction Acoustic Calibrator	C1005490

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	94.3	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L _A	A	Fast	94.00	1	94.3 (Ref.)
				104.00		104.3
				114.00		114.3

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

- 6.2 Time Weighting

- 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	94.3	Ref.
			Slow			94.2	± 0.1

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _A	A	Fast	94.00	31.5 Hz	55.3	-39.4 ± 1.5
					63 Hz	68.4	-26.2 ± 1.5
					125 Hz	78.4	-16.1 ± 1.0
					250 Hz	85.8	-8.6 ± 1.0
					500 Hz	91.1	-3.2 ± 1.0
					1 kHz	94.3	Ref.
					2 kHz	95.3	+1.2 ± 1.0
					4 kHz	94.5	+1.0 ± 1.0
					8 kHz	90.5	-1.1 (+1.5 ; -3.0)
					12.5 kHz	85.0	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _C	C	Fast	94.00	31.5 Hz	91.5	-3.0 ± 1.5
					63 Hz	93.7	-0.8 ± 1.5
					125 Hz	94.2	-0.2 ± 1.0
					250 Hz	94.4	0.0 ± 1.0
					500 Hz	94.4	0.0 ± 1.0
					1 kHz	94.3	Ref.
					2 kHz	94.0	-0.2 ± 1.0
					4 kHz	92.8	-0.8 ± 1.0
					8 kHz	88.7	-3.0 (+1.5 ; -3.0)
					12.5 kHz	82.4	-6.2 (+3.0 ; -6.0)

6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Freq. (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
20 - 110	L _{Aeq}	A	60 sec.	4	1	1/10 ³	110.0	80	80.7	± 1.0
			5 min.					70	70.7	± 1.0

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C103778

Calibration Report

Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value : 94 dB : 31.5 Hz - 125 Hz : ± 0.35 dB
250 Hz - 1 kHz : ± 0.30 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
12.5 kHz : ± 0.70 dB
104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 4 of 4



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C105886

Certificate of Calibration

This is to certify that the equipment

Description : Sound Level Meter

Manufacturer : Rion

Model No. : NL-31

Serial No. : 00983400

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C105886.*

The equipment is supplied by

Co. Name : Envirotech Services Co.

*Address : Shop 6, G/F., Casio Mansion, 209 Shaaukeiwan Road,
Hong Kong*

Date of Issue : 26 October 2010

Certified by :

K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C105886

Calibration Report

ITEM TESTED

DESCRIPTION : Sound Level Meter
MANUFACTURER : Rion
MODEL NO. : NL-31
SERIAL NO. : 00983400

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$
LINE VOLTAGE : ---

RELATIVE HUMIDITY : $(55 \pm 20)\%$

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 25 October 2010

JOB NO. : IC10-2726


TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


L L Cheung

Date : 26 October 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
Tel: 2927 2606 Fax: 2744 8986 E-mail: callab@suncreation.com Website: www.suncreation.com

Page 1 of 4

Report No. : C105886

Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C100067
CL281	Multifunction Acoustic Calibrator	C1006860

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading	IEC 61672 Class 1 Spec.
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
30 - 120	L _A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)
30 - 120	L _A	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.1

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading	IEC 61672 Class 1 Spec.
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	(dB)	(dB)
30 - 120	L _A	A	Fast	94.00	1	94.0	Ref.
			Slow			93.9	± 0.3

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Calibration Report

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _A	A	Fast	94.00	63 Hz	67.6	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.5
					250 Hz	85.2	-8.6 ± 1.4
					500 Hz	90.7	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.3	+1.2 ± 1.6
					4 kHz	95.1	+1.0 ± 1.6
					8 kHz	93.0	-1.1 (+2.1 ; -3.1)
					12.5 kHz	90.1	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _C	C	Fast	94.00	63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.0	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.9	-0.2 ± 1.6
					4 kHz	93.4	-0.8 ± 1.6
					8 kHz	91.1	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.3	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
Tel: 2927 2606 Fax: 2744 8986 E-mail: callab@suncreation.com Website: www.suncreation.com

Report No. : C105886

Calibration Report

Remarks : - Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB
250 Hz - 500 Hz : ± 0.30 dB
1 kHz : ± 0.20 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
12.5 kHz : ± 0.70 dB
104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
Tel: 2927 2606 Fax: 2744 8986 E-mail: callab@suncreation.com Website: www.suncreation.com

Page 4 of 4

Annex B2

Results of Noise Monitoring

Annex B2
Operational Noise Monitoring Results

Monitoring Location: AON1 Open area adjacent to Police Training School

Date	Weekdays/ Public Holiday (WD/PH)	Measurement Period, hours		Measured Noise Level ^[1] , dB(A)			Noise Criteria, L _{eq(30mins)} , dB(A)	Remark / Other Noise Source(s)
		Start	End	Daily Operational Noise Level, L _{eq} , 30min	Lagoon Night Show Noise Level, L _{eq} , 30min	Background Noise Level, L _{eq} , 15min		
29-May-11	PH	1850	2000	67.6	65.3	65.1	60	Note ^{[1] & [2]}
31-May-11	WD	1920	2030	62.4	63.2	63.5	60	-
05-Jun-11	PH	1920	2030	66.0	65.7	64.8	60	Note ^{[1] & [2]}
07-Jun-11	WD	1920	2030	60.6	63.8	64.4	60	-
12-Jun-11	PH	1920	2030	66.9	65.8	65.8	60	Note ^{[1] & [2]}
14-Jun-11	WD	1920	2030	61.9	62.3	62.0	60	-
19-Jun-11	PH	1920	2030	65.4	63.9	64.5	60	Note ^{[1] & [2]}
21-Jun-11	WD	1920	2030	63.7	63.5	63.9	60	-

Monitoring Location: AON2 Roof of Old Canteen Building

Date	Weekdays/ Public Holiday (WD/PH)	Measurement Period, hours		Measured Noise Level ^[1] , dB(A)			Noise Criteria, L _{eq(30mins)} , dB(A)	Remark / Other Noise Source(s)
		Start	End	Daily Operational Noise Level, L _{eq} , 30min	Lagoon Night Show Noise Level, L _{eq} , 30min	Background Noise Level, L _{eq} , 15min		
29-May-11	PH	1850	2000	59.8	58.7	58.3	60	-
31-May-11	WD	1920	2030	58.6	60.6	62.3	60	-
05-Jun-11	PH	1920	2030	58.2	59.3	57.7	60	-
07-Jun-11	WD	1920	2030	58.8	59.1	57.4	60	-
12-Jun-11	PH	1920	2030	58.0	59.2	57.8	60	-
14-Jun-11	WD	1920	2030	62.7	68.8	67.1	60	Note ^{[1] & [3]}
19-Jun-11	PH	1920	2030	59.4	60.2	58.8	60	-
21-Jun-11	WD	1920	2030	60.9	59.4	58.1	60	-

Monitoring Location: AON3 Woodgreen Estate

Date	Weekdays/ Public Holiday (WD/PH)	Measurement Period, hours		Measured Noise Level ^[1] , dB(A)			Noise Criteria, L _{eq(30mins)} , dB(A)	Remark / Other Noise Source(s)
		Start	End	Daily Operational Noise Level, L _{eq} , 30min	Lagoon Night Show Noise Level, L _{eq} , 30min	Background Noise Level, L _{eq} , 15min		
29-May-11	PH	1850	2000	64.4	60.9	61.5	55	Note ^{[1] & [4]}
31-May-11	WD	1920	2030	66.1	64.2	64.0	55	Note ^{[1] & [4]}
05-Jun-11	PH	1920	2030	64.2	62.4	61.9	55	Note ^{[1] & [4]}
07-Jun-11	WD	1920	2030	62.7	61.7	61.2	55	Note ^{[1] & [4]}
12-Jun-11	PH	1920	2030	62.8	64.5	64.9	55	-
14-Jun-11	WD	1920	2030	66.1	65.7	66.2	55	-
19-Jun-11	PH	1920	2030	63.0	65.3	65.7	55	-
21-Jun-11	WD	1920	2030	66.3	64.5	64.9	55	Note ^{[1] & [4]}

Monitoring Location: AON4 Manly Villa

Date	Weekdays/ Public Holiday (WD/PH)	Measurement Period, hours		Measured Noise Level ^[1] , dB(A)			Lagoon Night Show Noise Level (Background Corrected), L _{eq,30min}	Noise Criteria, L _{eq(30mins)} , dB(A)	Remark / Other Noise Source(s)
		Start	End	Daily Operational Noise Level, L _{eq,30min}	Lagoon Night Show Noise Level, L _{eq,30min}	Background Noise Level, L _{eq,15min}			
29-May-11	PH	1850	2000	54.2	52.1	51.7	41.5	55	-
31-May-11	WD	1920	2030	53.9	54.0	55.3	Negligible	55	-
05-Jun-11	PH	1920	2030	55.1	54.8	54.1	46.8	55	-
07-Jun-11	WD	1920	2030	55.7	54.7	53.0	49.6	55	-
12-Jun-11	PH	1920	2030	54.0	54.2	52.9	48.1	55	-
14-Jun-11	WD	1920	2030	53.9	54.8	53.2	49.5	55	-
19-Jun-11	PH	1920	2030	54.1	55.3	54.0	49.3	55	-
21-Jun-11	WD	1920	2030	57.9	58.0	58.0	36.9	55	-

Monitoring Location: AON5 Hau Yuen


Date	Weekdays/ Public Holiday (WD/PH)	Measurement Period, hours		Measured Noise Level ^[1] , dB(A)			Lagoon Night Show Noise Level (Background Corrected), L _{eq,30min}	Noise Criteria, L _{eq(30mins)} , dB(A)	Remark / Other Noise Source(s)
		Start	End	Daily Operational Noise Level, L _{eq,30min}	Lagoon Night Show Noise Level, L _{eq,30min}	Background Noise Level, L _{eq,15min}			
29-May-11	PH	1850	2000	58.7	58.1	58.4	Negligible	55	-
31-May-11	WD	1920	2030	58.8	56.3	56.7	Negligible	55	-
05-Jun-11	PH	1920	2030	59.7	57.5	57.9	Negligible	55	-
07-Jun-11	WD	1920	2030	59.1	58.9	57.8	52.1	55	-
12-Jun-11	PH	1920	2030	59.3	57.3	57.2	42.1	55	-
14-Jun-11	WD	1920	2030	59.0	56.7	55.8	49.3	55	Note ^{[1] & [4]}
19-Jun-11	PH	1920	2030	57.8	58.2	57.9	46.7	55	-
21-Jun-11	WD	1920	2030	59.0	57.0	55.3	52.1	55	Note ^{[1] & [4]}

Notes:


- [1] Bolded value indicates exceedance over the noise criteria.
Negligible refers to the measured impact noise levels lower than the background noise levels.
[2] The exceedances were due to the high level of background noise from visitors and traffic on public holidays, especially on 29 May, 5, 12 and 19 Jun 2011, which were public holidays.
[3] The exceedance was due to the noise from construction works near the Cable Car Terminal on 14 June 2011, CNP No.GW-RS0314-11.
[4] The exceedances at AON3 and AON5 were due to traffic noise from Shouson Hill Road.

Annex B3

Graphical Presentation of Noise Monitoring Results

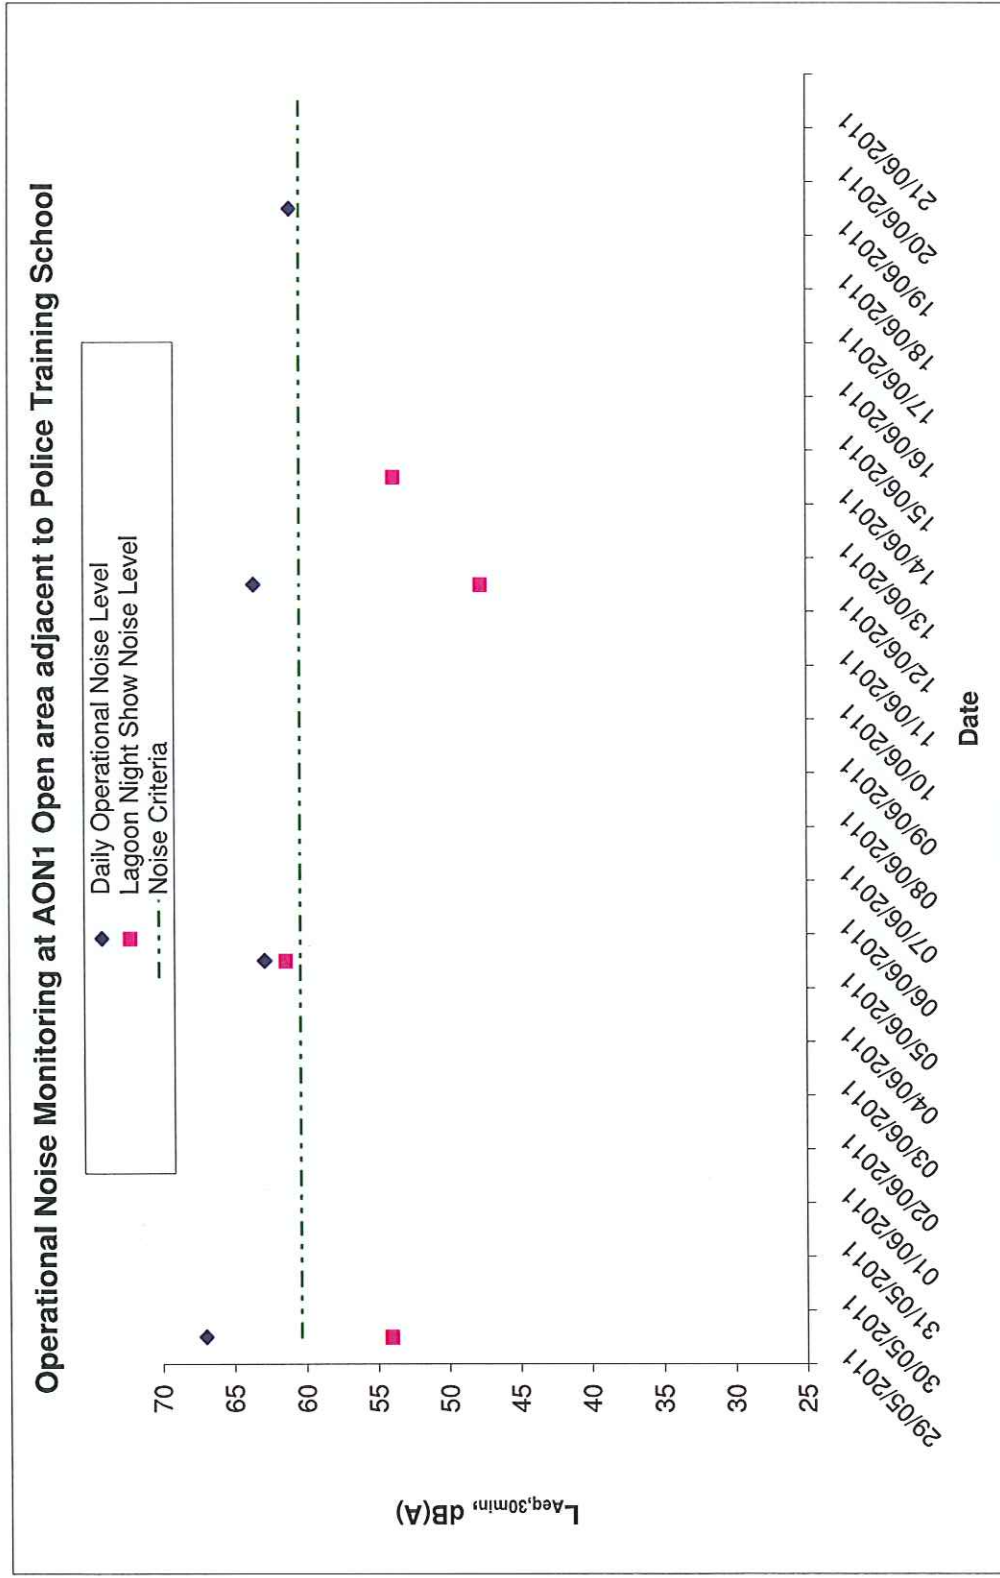


Note: The exceedances were due to the high level of background noise from visitors and traffic on public holidays, especially on 29 May, 5, 12 and 19 June 2011, which were public holidays.

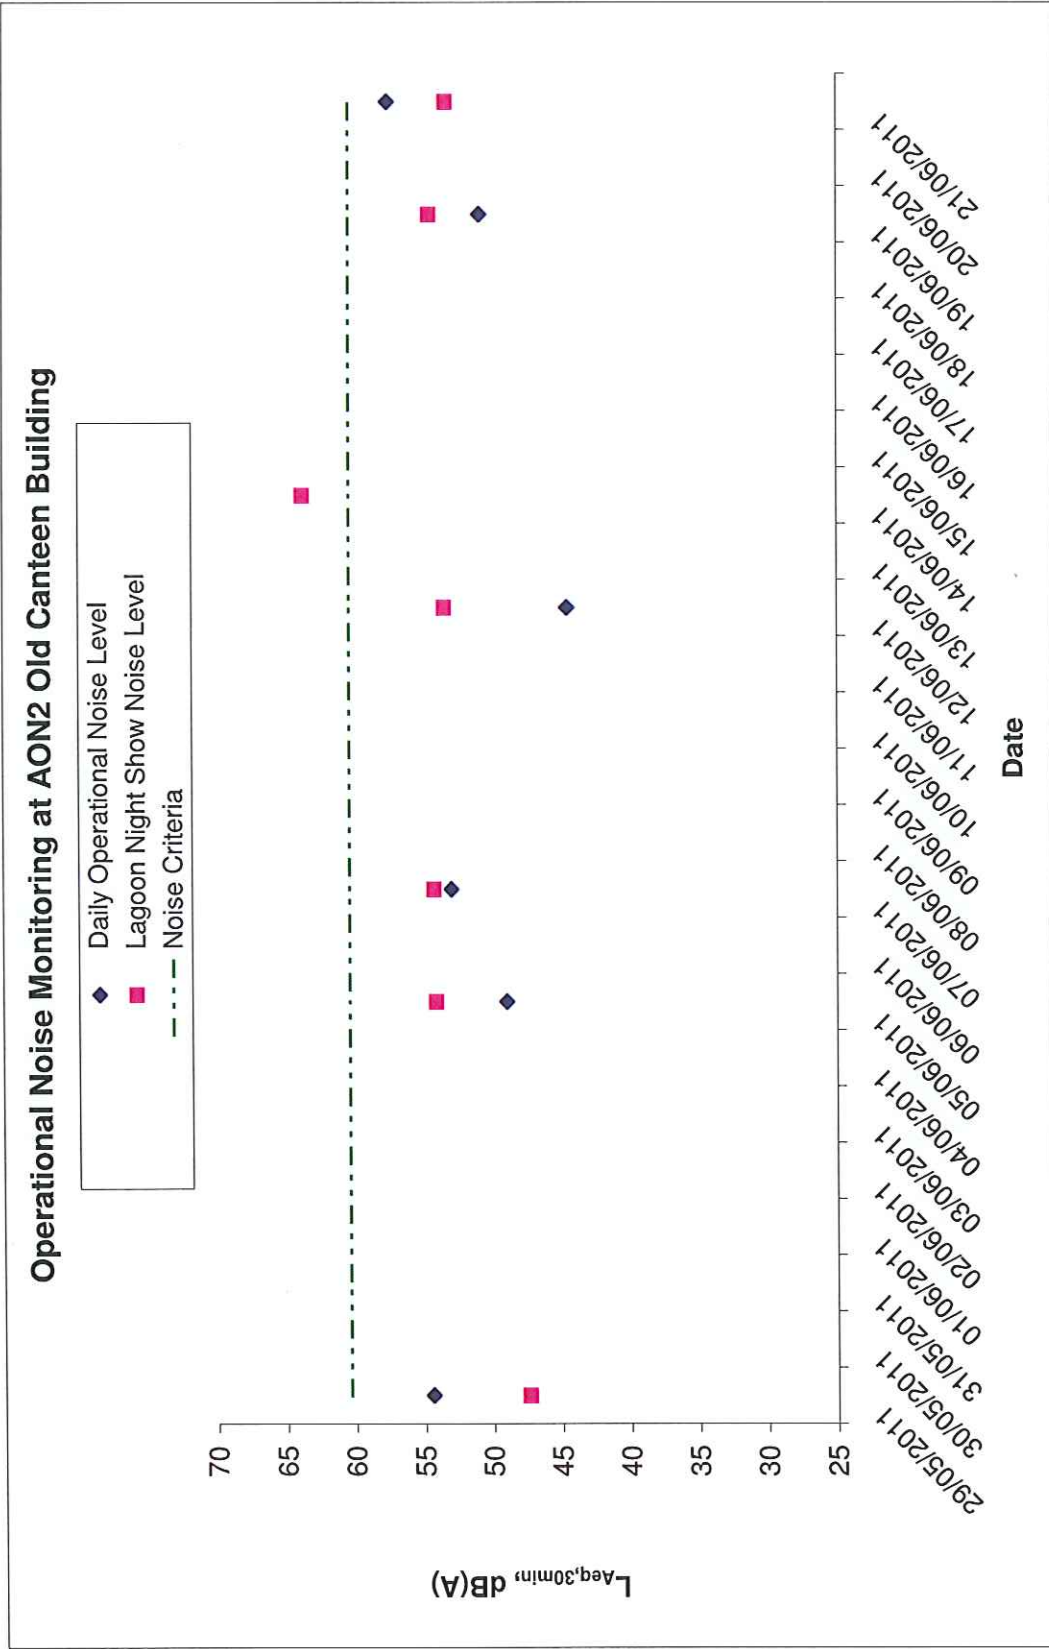


Note: The exceedance was due to the noise from construction works near the Cable Car Terminal on 14 June 2011, CNP No. GW-RS0314-11.


Operational Noise Monitoring at AON3 Woodgreen Estate

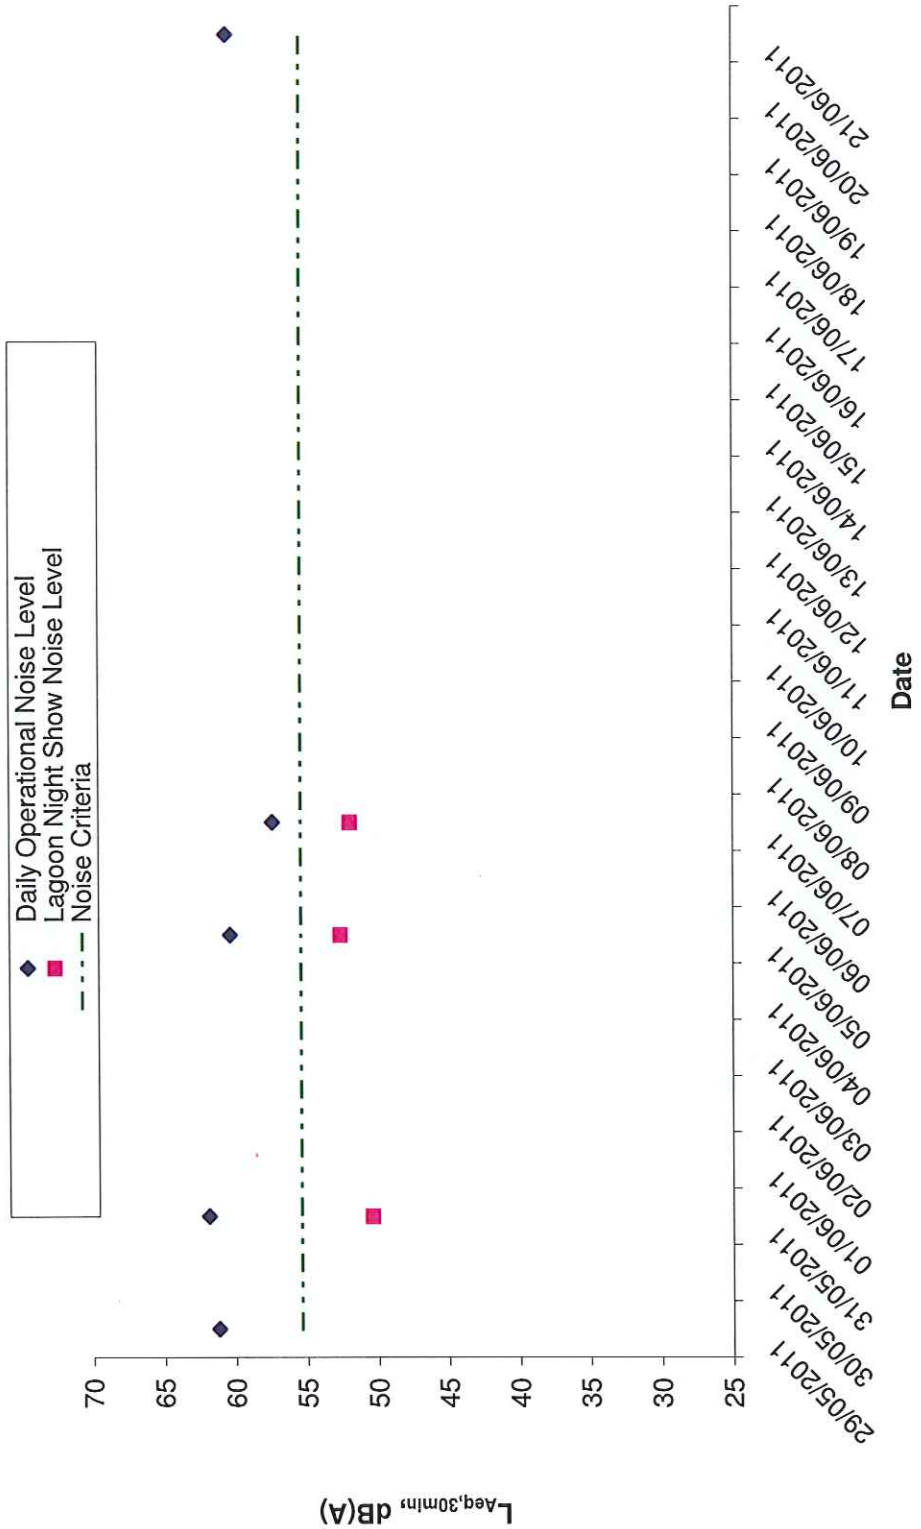

Note: The exceedances were due to the traffic noise from Shouson Hill Road

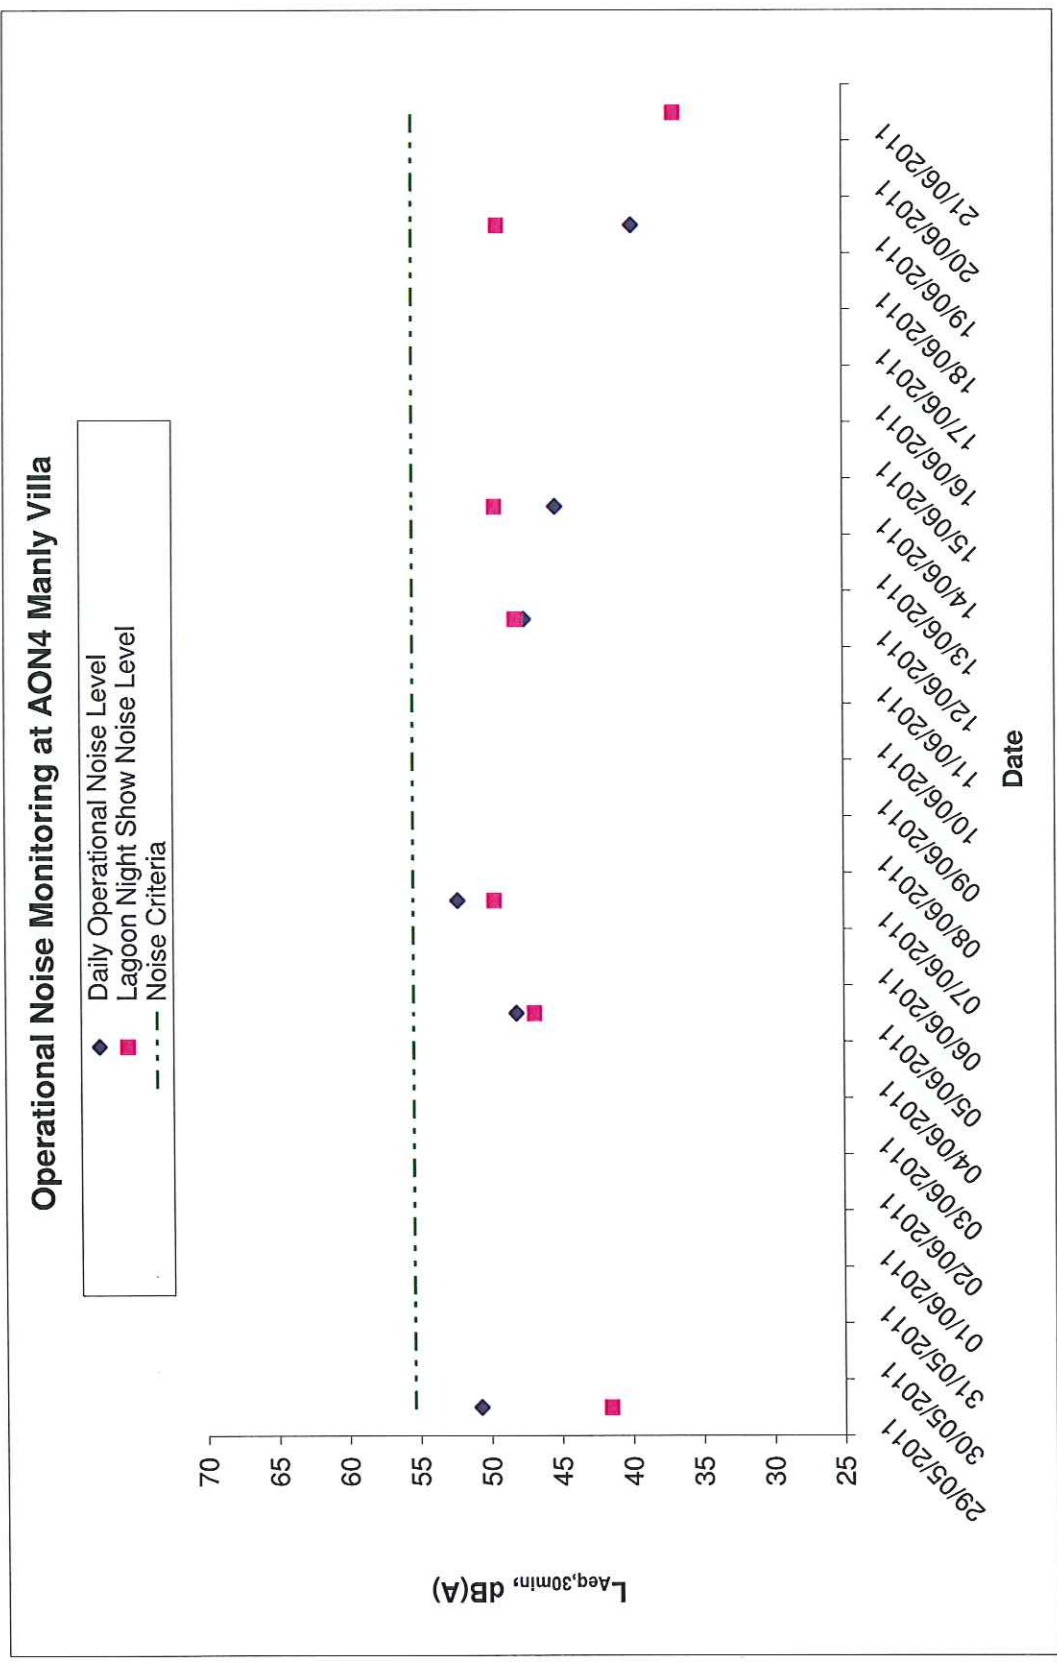

Operational Noise Monitoring at AON5 Hau Yuen

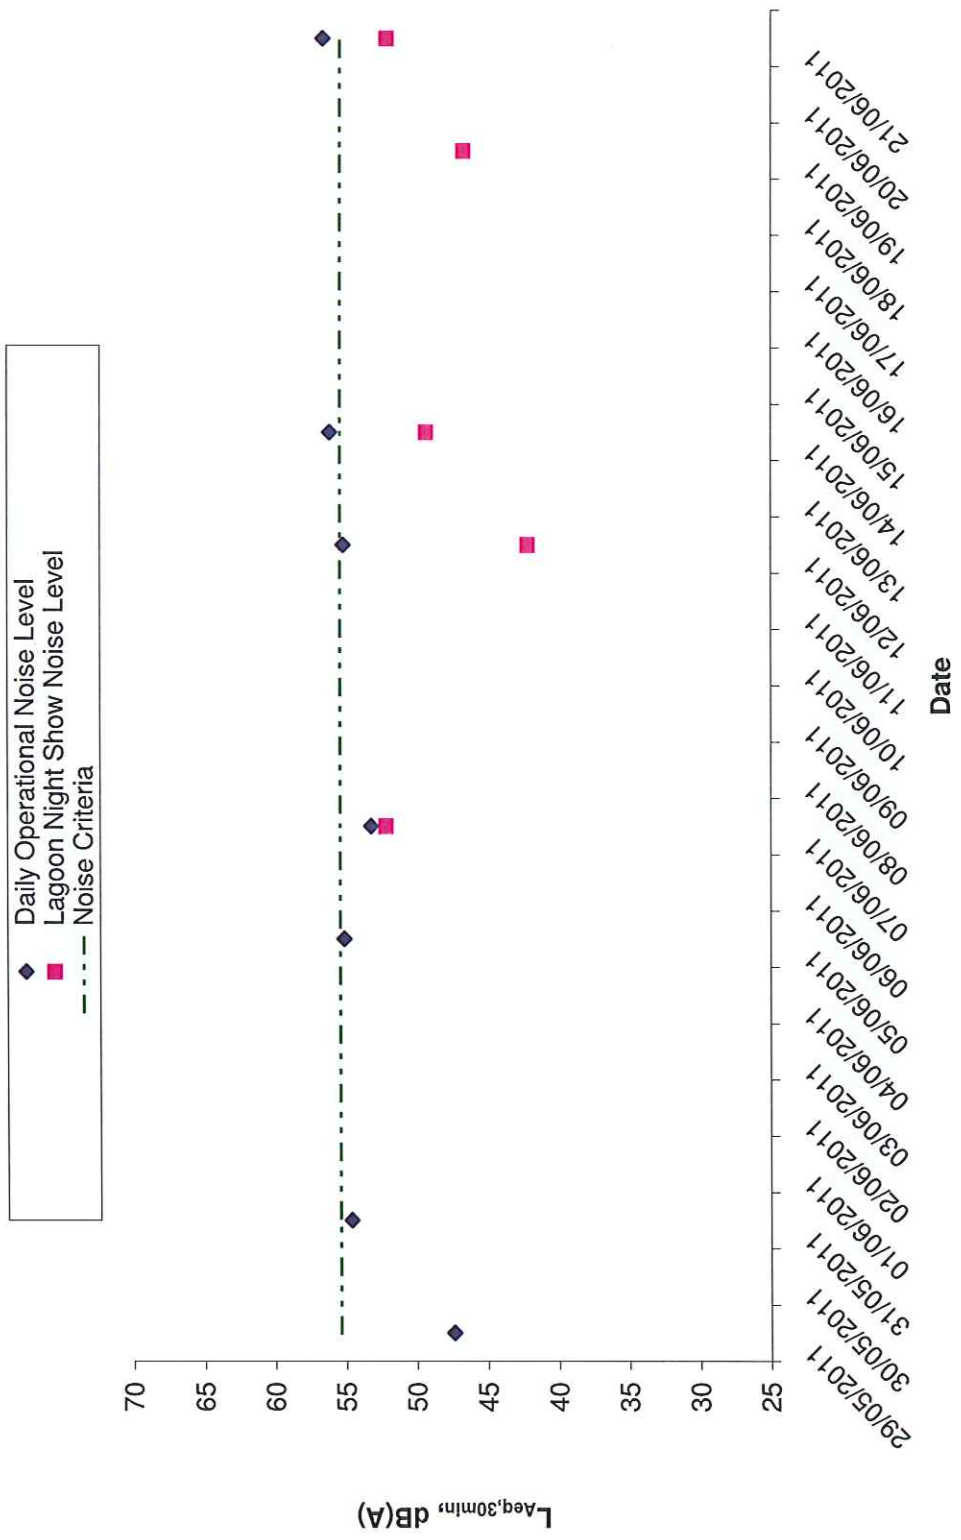

Note: The exceedances were due to traffic noise from Shouson Hill Road

Annex B4

Construction Noise Permit



Contractor Submittal (SUB)
File : 22.02



W. Hing Construction Co. Ltd.
永興聯合建築有限公司

To: Project Manager's Representative

Contract: A501 - HONG KONG STREET

Ref. No.: A501 / SUB / ST/ 000066

Location: Site Subject : Construction Noise Permit

In accordance with Specification Clause(s) N/A, we submit the following document: -

- | | |
|----------------------|-------------------------|
| () Material | () General Obligations |
| () Shop Drawing | () Safety & Health |
| () Sample | () Environmental |
| () Programme | () Quality |
| () Method Statement | () Testing Report |
| (X) Others | |

Purpose of Submission ☐ for review ☒ for information ☒ for record

Type of Submission ☐ Civil & Structural ☐ Architectural ☐ E&M ☒ others

Details:

We submit herewith the Construction Noise Permit for your record.

The date of commencement from 15 May 2011 to 14 November 2011.

Your earliest response is requested.

~~Ian Malpass~~ / Wesley Lo

18 April 2011

Date

*Delete as appropriate

本署傳真
OUR REF: GW-RS0314-11
來函編號
YOUR REF: A501/20.05/038
電話
TEL NO: 2516 1782
圖文傳真
FAX NO: 2960 1761
網址
HOME PAGE: <http://www.epd.gov.hk/>

Environmental Protection Department
Environmental Compliance Division
Regional Office (South)
2/F., Chinachem Exchange Square
1 Hoi Wan Street
Quarry Bay, Hong Kong

環境保護署
環保法規管理科
區域辦事處(南)
香港鰂魚涌
海灣街一號
華登交易廣場二樓

Registered Post

13 April 2011

To: W. HING CONSTRUCTION COMPANY LIMITED
14/F. YAU LEE CENTRE,
45 HOI YUEN ROAD,
KWUN TONG,
KOWLOON

Dear Sir,

**Notice of Issue of Construction Noise Permit pursuant
to Section 8(6) of the Noise Control Ordinance (Cap. 400)**

I write to inform you that, under Section 8(6) of the Noise Control Ordinance, the Authority has decided to issue a construction noise permit in respect of your application, which was received by the Authority on 30 March 2011, for the use of powered mechanical equipment for carrying out construction work at **Cable Car Terminal, Ocean Park, Aberdeen, Hong Kong.**

The construction noise permit No. GW-RS0314-11 is enclosed.

You are strongly advised to read the conditions of the permit carefully and to ensure compliance with these conditions. Any breaching of the conditions may lead to cancellation of the permit, subsequent prosecution action and the Authority's refusal to issue further permit for the above construction site.

If you have any query, please contact Mr. Tang Wai Sing at 25161810 or the undersigned.

Yours faithfully,


(WONG Ho-ying)
for Authority

FORM 2
NOISE CONTROL ORDINANCE
(Chapter 400)
SECTION 8(9)

(2 of 18)

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RS0314-11

To : W. HING CONSTRUCTION COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed :

Full address : Cable Car Terminal, Ocean Park, Aberdeen, Hong Kong

Lot No. -----

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. PART/WHOLE of the site falls WITHIN/OUTSIDE a designated area.
3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

Identification code of item of powered mechanical equipment (if applicable)	Description of item of powered mechanical equipment	No. of units
CNP 102	Generator, silenced, 75 dB(A) at 7 m	One
CNP 283	Water pump, submersible (electric)	One

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of Commencement : 15 May 2011 at 0700 hours

Days and hours: 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday [but note Condition 3.d.1. below for the operating hours within which the use of the above listed powered mechanical equipment is allowed].

This part of the permit expires on : 14 November 2011 at 2300 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.
d. Other conditions imposed on the use of the powered mechanical equipment:

Refer to attached sheet

4. Prescribed Construction Work

- a. Type of prescribed construction work which may be carried out inside the site boundary:

Identification code of type of prescribed construction work	Description of type of prescribed construction work
	NIL

- b. Validity of the construction noise permit for the carrying out of the prescribed construction work:

Date and time of commencement : 15 May 2011 at 0700 hours
 Days and hours: 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday.

This part of the permit expires on : 14 November 2011 at 2300 hours

- c. Site layout plan(s), endorsed by the Authority, may be attached with the permit to indicate the locations permitted for the carrying out of prescribed construction work described in this permit. The layout plan(s) is(are) required to be kept on the construction site and made available for inspection by the Authority.

- d. Other conditions imposed on the carrying out of the prescribed construction work:

Not applicable

5. This construction noise permit or a copy thereof must be displayed on the construction site at all vehicular site entrances/exits for public information.

Dated this 13th day of April 2011

Signed:

(WONG Ho-ying)

for Authority

* Delete as necessary

《噪音管制條例》
(第400章)
第3(9)條

[第 11 頁]

建築噪音許可證
為進行建築工程（撞擊式打樁除外）
而使用機動設備及／或進行訂明建築工程

建築噪音許可證編號： GW-RS0314-11

致：永興聯合建築有限公司

本建築噪音許可證是按照《噪音管制條例》第8條的規定而發出的，現准予使用機動設備以進行撞擊式打樁工程以外的建築工程及／或進行訂明建築工程，但須受以下條件規限。若不按照該等條件進行建築工程，許可證可遭撤銷，而且會受到檢控。

條 件

1. 可使用機動設備及／或進行訂明建築工程的建築地盤：

詳細地址：香港香港仔海洋公園纜車站

地段編號：-----

地盤範圍（即可使用機動設備及進行訂明建築工程的地方範圍）已描劃於夾附的圖則上，而該圖則是本建築噪音許可證的一部分。

2. 該地盤部份／全部位於指定範圍之內／外。
3. 機動設備

- a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識別代碼 (如適用的話)	各項機動設備的說明	數目
CNP 102	發電機，低噪音型在7米距離時75分貝(A)	壹
CNP 283	潛水泵（電動）	壹

- b. 可使用機動設備的建築噪音許可證有效期：

生效日期及時間：二零一一年五月十五日 上午七時

日期及時間：公眾假日（包括星期日）的凌晨零時至晚上十二時，公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時 [但須注意條件3.d.1.有關可以使用上列機動設備的時間]。

此部分許可證屆滿日期及時間：二零一一年十一月十四日 晚上十一時

日期

時間

- c. 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各一幀，供監督隨時查看；該等照片須經監督認可。
d. 規限使用機動設備的其他條件：

參見附頁

2. 訂明建築工程

a. 在地盤範圍內可進行的訂明建築工程：

訂明建築工程的識別代碼	訂明建築工程的類別的說明
	無

b. 可進行訂明建築工程的建築噪音許可證有效期：

生效日期及時間：二零一一年五月十五日 上午七時

日期及時間：公眾假日（包括星期日）的凌晨零時至晚上十二時，公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時。

此部分許可證屆滿日期及時間：二零一一年十一月十四日 晚上十一時

日期 時間

c. 本許可證可夾附經監督認可的地盤圖則，以顯示本許可證准予進行訂明建築工程的地點。該地盤圖則須存放於建築地盤供監督隨時查看。

d. 規限進行訂明建築工程的其他條件：

不適用

5. 本建築噪音許可證或其副本必須展示於建築地盤的所有車輛進出口處，給予公眾人士參閱。

日期：二零一一年四月十三日

簽署：



監督

（黃可瑩 代行）

* 刪去不適用者

Sheet Attached to Construction
Noise Permit No. GW-RS0314-11

3.d. Other conditions imposed on the use of the powered mechanical equipment:

1. The powered mechanical equipment listed in condition 3.a. shall only be operated during the hours shown below:
General holidays (including Sundays) between 0700 – 1900 hours.
Any day not being a general holiday between 1900 – 2300 hours.

Signed : _____
(WONG Ho-ying)
for Authority

頁一，共一頁

建築噪音許可證
編號GW-RS0314-11的附頁


3.d. 規限使用機動設備的其他條件:

1. 列在條件3.a.內的機動設備只可於以下時間內使用:
公眾假日(包括星期日)的上午七時至下午七時。
公眾假日以外的任何一日下午七時至晚上十一時。




簽署 : _____
監督
(黃可瑩 代行)


建築噪音許可證編號 GW-RS0314-11 的相片
Photograph(s) Attached to Construction Noise Permit No. GW-RS0314-11

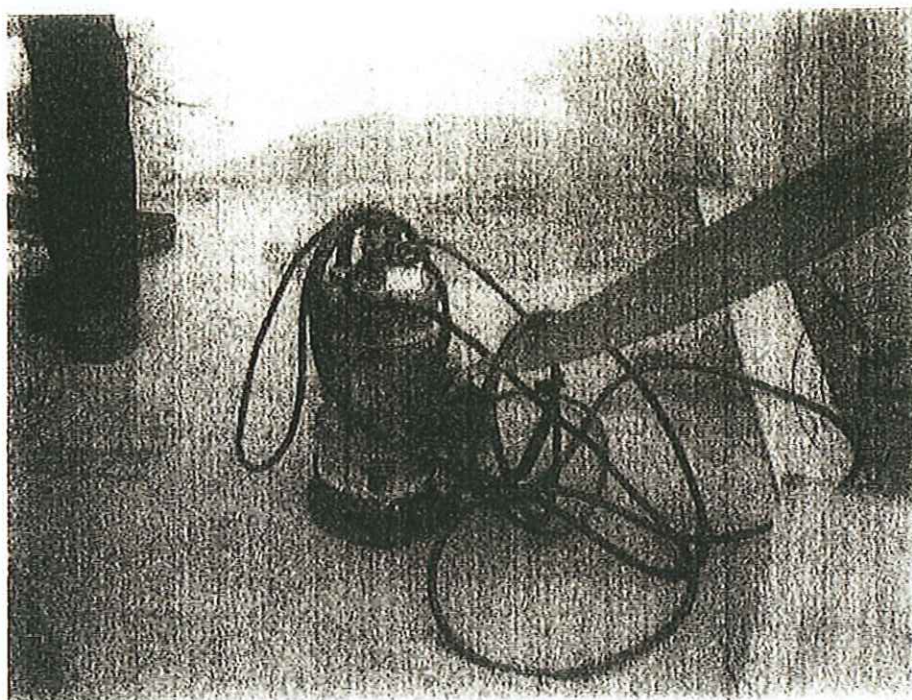

CNP 283 潛水泵（電動）
Water pump, submersible (electric)

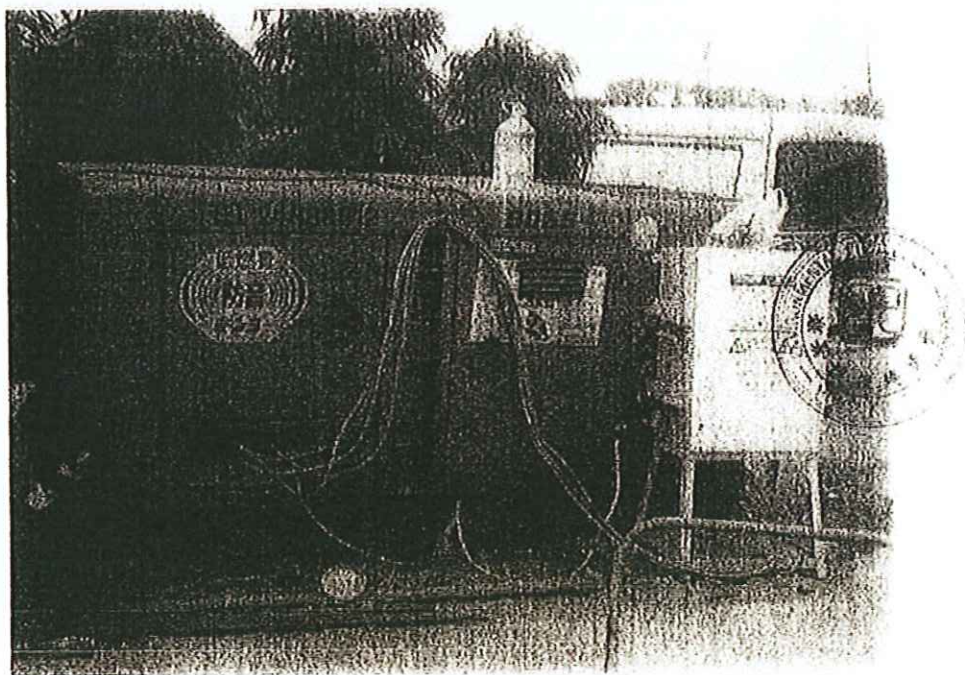

CNP 102 發電機，低噪音型在7米距離時75分貝（A）
Generator, silenced, 75 dB(A) at 7 m

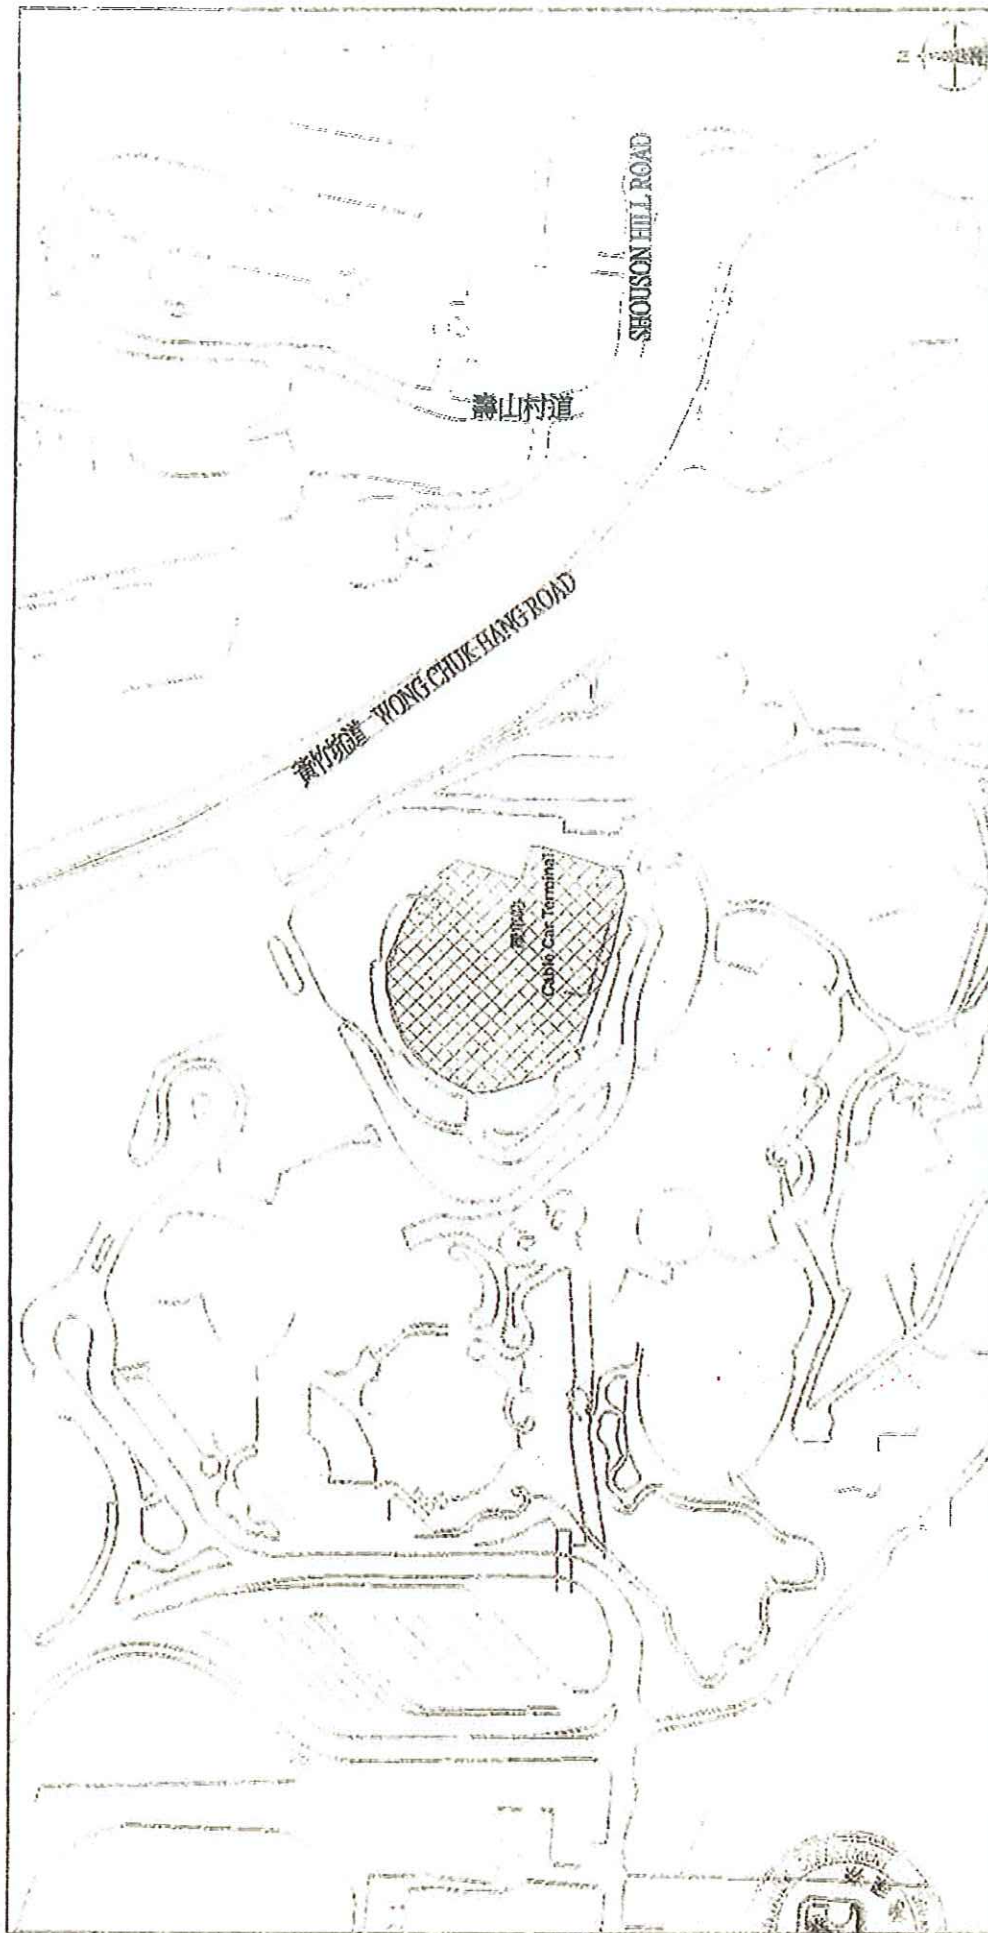

環境保護署

噪音管制監督

圖例 Legend

Environmental Protection Department

Noise Control Authority

建築地盤 Construction Site

建築噪音許可證編號 GW-RS0314-11 的附圖

比例 Scale 1:2,500

Plan attached to Construction Noise Permit No. GW-RS0314-11

