

Drainage Service Department

Monthly Environmental Monitoring & Auditing report for

Contract No.DC/2006/11

Drainage Improvement in Southern Lantau

October 2008

Environmental Pioneers & Solutions Limited

8/F, Chaiwan Industrial Centre Building


20 Lee Chung Street, Chaiwan, Hong Kong

Tel: 2889 0568


Fax: 2856 2010

APPROVAL SHEET

Prepared and Certified by: ET Leader (Environmental Pioneers & Solutions Limited)

Signature: 
Miss Patricia Chung
(ET* Leader)

Date: 14 NOV 2008

Signature: 
Mr. Vincent Zai
(Ecologist)

Date: 14 NOV 2008

* ET – Environmental Team

TABLE of CONTENT

TABLE of CONTENT	ii
EXECUTIVE SUMMARY	iv
1. Introduction.....	1
2. Project Information	1
2.1 Construction program	1
2.2 Project Organization	1
2.3 Key Personal Contact information chart.....	2
3. Construction Stage	3
3.1 Construction Activities in the reporting month.....	3
3.2 Construction Activities for the coming month.....	3
3.3 Environmental Status	3
4. Noise Monitoring	4
4.1 Monitoring Parameters and Methodology	4
4.2 Monitoring Equipment.....	4
4.3 Monitoring Locations.....	5
4.4 Monitoring Results and Interpretation	7
4.5 Action and Limit level for Construction noise	7
4.6 Noise Mitigation Measures	9
5. Water Monitoring.....	10
5.1 Water Quality Monitoring Parameters and methodology	10
5.2 Monitoring Equipment.....	10
5.3 Monitoring Locations.....	11
5.4 Monitoring Frequency	13
5.5 Monitoring Results and Interpretation	13
5.6 Action and limit level for Water Quality.....	15
5.7 Water Quality Mitigation Measures	17
5.8 Water Monitoring Schedule for the Next reporting period.....	17
6. Ecology Monitoring	18
6.1 Ecological Monitoring Parameters	18
6.2 Monitoring Equipment and Methodology	19
6.3 Monitoring Locations.....	20
6.4 Monitoring Frequency	23
6.5 Monitoring results	23
6.6 Action and Limit level for Monitoring of White-shouldered Starlings	32

6.7	Ecological monitoring Schedule	32
7.	Action taken in Event of Exceedence	33
8.	Construction waste disposal.....	34
	Table 8.1 Summary of Construction Waste Disposal.....	34
9.	Status of Permits and Licenses obtained.....	35
10.	Complaint Log	35
11.	Site Environmental Audits	36
	11.1 Site Inspection.....	36
	11.2 Compliance with legal and Contractual requirement.....	37
	11.3 Environmental Complaint and follow up actions.....	37
12.	Future key issues.....	38
13.	Conclusions.....	38

APPENDIXES

Appendix A	Key Personal Contact information chart
Appendix B	Calibration Certificates for measuring instruments
Appendix C1	Plant species recorded at Pak Ngan Heung River (N)
Appendix C2	Plant species recorded at Pak Ngan Heung River (S)
Appendix C3	Plant species recorded at Luk Tei Tong River
Appendix C4	Ecological Water Monitoring results (on-site measurement)
Appendix C5	Ecological Water Monitoring results (lab-report)
Appendix D	Construction Noise Monitoring Data Sheet
Appendix E1	Water Quality Monitoring Data Sheet
Appendix E2	Water Quality Monitoring Lab report
Appendix F	Monitoring Schedule for Sept 2008
Appendix G	Construction Programme and location plan
Appendix H	Implementation status of environmental protection / mitigation measures
Appendix I	Graphical plot of water quality monitoring results (SS, DO, turbidity)
Appendix J	Graphical plot of noise monitoring results

EXECUTIVE SUMMARY

This is the third monthly environmental Monitoring and audit (EM&A report for “Drainage Improvement in Southern Lantau Investigation”. The environmental permit number is “EP-237/2005/A”. The report concludes the impact monitoring for the activities undertaken during the period of 1st October 2008 to 31st October 2008. The major activities in this reporting month include construction work of box culvert at Pak Ngan Heung River (PNHR) & construction work of U-channel at Ling Tsui Tau.

Noise, water quality and ecological monitoring were performed. Results obtained were checked against the previously established Action / Limit (A/L) levels. Additionally, the implementation status of environmental mitigation measures, event/ action plan and environmental complaint handling procedures were inspected during weekly site environmental audit.

In general, waste management was satisfactory during the reporting month.

Impact monitoring for construction noise was conducted in the reporting period. No exceedance of A/L level was reported.

Furthermore, impact monitoring for water quality was conducted. Most of the monitoring results are within established A/L level, except 6 exceedance events of Turbidity, Dissolved Oxygen and Suspended Solid were reported. However there is no river construction works has been commenced yet.

During ecological monitoring survey, no White-shouldered Starling was recorded breeding in the watch tower. And there was no sign of disturbance from the Project to the watch tower as no construction work of the Project were conducted near the tower in November 2008. The breeding season of White-shouldered Starling is probably over in this time of the year. In addition, no disturbance on the flora and fauna in the river channels were observed during the ecological monitoring.

Furthermore, there was no complaint, notification of any summons and successful prosecutions against the project received during the reporting period.

Key construction activity in the coming month will be construction of box culvert at PNHR, and site clearance work at Luk Tei Tong (LTT) marsh. It is expected that noise impacts and waste disposal will be generated on-site, and certain ecological and water impacts may be resulted from site clearance work at LTT. With reference to the EM&A manual and mitigation measure report, mitigation measures are proposed to be taken, if necessary.

The environmental performance of the project was generally satisfactory.

1. Introduction

This is the third monthly Environmental Monitoring and Audit (EM&A) Report for “Drainage Improvement in Southern Lantau Investigation” project (Environmental Permit No. EP-237/2005/A)

2. Project Information

2.1 Construction program

The “Drainage Improvement in Southern Lantau Investigation” project will be completed by June 2009. The project comprises the following:

- Construction of approximately 80m long gabion with natural bed in Pak Ngan Heung River, approximately 180m of three cells 3m x 2m box culvert and approximately 100m of rectangular channel at Pak Ngan Heung River;
- Construction of approximately 250m of 0.75m wide U-Channel at Ling Tsui Tau Village in Mui Wo;
- Construction of bypass channel of about 350m and 240m long of gabion channels at Luk Tei Tong River respectively; and
Widening three existing bottlenecks with gabion lined at Tai Tei Tong River

Appendix G shows the construction program and location plan of the project.

2.2 Project Organization

The Main Contractor, Yick Hing Construction Company Limited, has commissioned Environmental Pioneers & Solutions Limited as the Environmental Team, which comprises the environmental team leader and the environmental technicians to undertake the environmental monitoring and audit work for this project.

The environmental management structure and is shown in Fig 2.2.1.

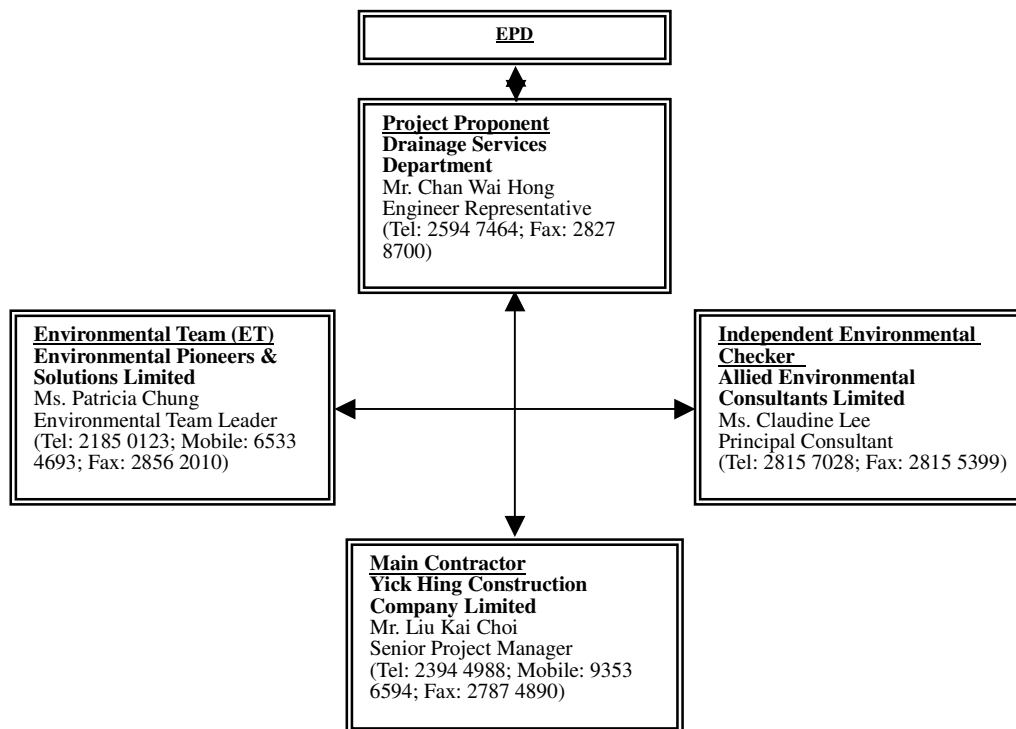


Figure. 2.2.1 Environmental Management structure for the project

2.3 Key Personal Contact information chart

Detailed contact of key persons involved in environmental aspect of the project is shown in appendix A.

3. Construction Stage

3.1 Construction Activities in the reporting month

Major activities in the reporting month include the construction works of box culvert along PNHR, construction for the U-channel at Ling Tsui Tau and site clearance work for LTT. These activities will be continued in the coming month.

3.2 Construction Activities for the coming month

Key construction activities for the coming month will include installation works of box culvert along PNHR, and site clearance works for LTT marsh.

3.3 Environmental Status

Appendix G shows the drawing of the project area.

Locations of the monitoring and control stations with environmental sensitive receivers are presented in Section 4.3, 5.3 and 6.3 for noise, water and ecological monitoring respectively.

4. Noise Monitoring

4.1 Monitoring Parameters and Methodology

The construction noise level was measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30minutes)}$ was used as the monitoring parameter for the impact monitoring in the time period between 0700 to 1900 hours on normal weekdays. For all other time period, $L_{eq(5minutes)}$ was employed for comparison with the Noise Control Ordinance (NCO) criteria.

Noise measurement results obtained from each monitoring location were recorded in the Construction Noise Monitoring Data Sheet (Appendix D) immediately after the measurement. As supplementary information for data auditing, statistical results L_{10} and L_{90} were also be recorded for reference.

In case of non-compliance with the construction noise criteria, more frequent monitoring, as specified in the Action plan in table 4.5.2, shall be carried out. This additional monitoring shall be carried out until the recorded noise levels are rectified or proved to be irrelevant to the construction activities.

4.2 Monitoring Equipment

The sound level meters and calibrators comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum (TM) to the Noise Control Ordinance was deployed as monitoring equipment for noise measurement.

Noise measurement was not be made in the presence of fog, rain, wind with a steady speed exceeding $5ms^{-1}$ or wind with gust exceeding $10ms^{-1}$. Thus wind speed was checked by the portable wind speed indicator capable of measuring the wind speed in m/s. Table 4.2.1 summarizes the equipment list for noise monitoring

Table 4.2.1 Equipment List for Noise Monitoring

Equipment	Manufacturer & Model No.	Precision Grade	Qty
Integrated sound level meter	SVAN Model 949	IEC 651 Type 1 IEC 804 Type 1	1
Windscreen	Microtech gefell model W2	N/A	1
Acoustical calibrator	SVAN SV-30A	IEC 942 Type 1	1
Wind speed indicator	Kestrel K1000	N/A	1
Remarks: Calibration details for the sound level meter is given in Appendix B for reference			

4.3 Monitoring Locations

According to the Baseline Monitoring Report issued in May 2008 for the captioned project, four locations were alternative from the locations proposed in EM&A manual, were designated for baseline noise monitoring. For the data validation, impact noise monitoring was undertaken in the same locations during the construction phase of the project. The proposed monitoring locations are summarized in Table 4.3.1. Figure 4.3.1 shows the Noise Monitoring Locations

Noise measurement in each monitoring locations were taken at a point 1m from the exterior of the selected premises and at a height with no disturbance to the dweller and least obstructed view.

Table 4.3.1 Noise Monitoring Locations during Construction Phase

Identification No.	Noise Monitoring Locations
N1	No. 73, Village House, Ling Tsui Tau Tsuen (ground level)
N2	No. 31, Village House, Ling Tsui Tau Tsuen (ground level)
N3	Fence wall outside No. 5 village house adjacent to Luk Tei Tong River Outlet (ground level)
N4	No. 23, Village House, Tai Tei Tong River (ground level)

In accordance with the requirements in the EM&A manual, weekly impact monitoring was conducted. For the time period between 0700 and 1900 hours on normal weekdays, and noise parameter of $L_{eq(30minutes)}$ was measured. As if the construction works were carried out during restricted period (ie. 1900-2300, 2300-0700 of next day and Sundays / general holiday), impact monitoring that comprises 3 consecutive $L_{eq(5minutes)}$ would be carried out.

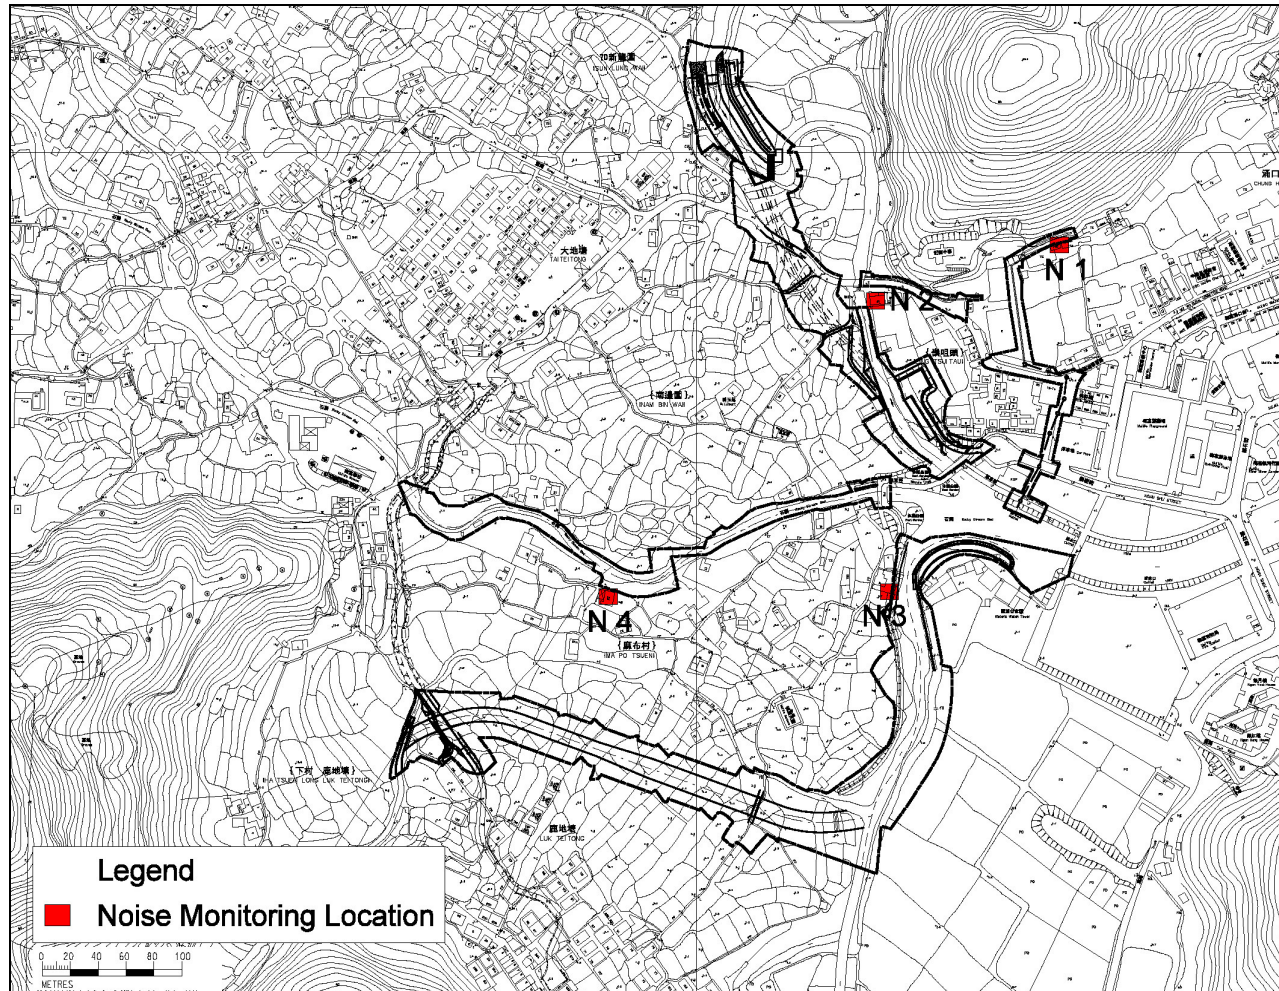


Figure 4.3.1 Impact noise monitoring locations

4.4 Monitoring Results and Interpretation

Relevant details of the noise monitoring results are presented in table 4.4.1. The results, ranged between 46.6 dB (A) and 65.6 dB (A), were within the limit levels and therefore, no exceedance was found.

Table 4.4.1 Noise monitoring results

Location	Parameter	Date	Time	L _{Aeq} dB(A)	Limit dB(A)	Exceedance	Weather
N1	L _{eq} 30mins	02/10/08	10:55	59.8	75	N	Sunny
N1	L _{eq} 30mins	08/10/08	11:20	53.9	75	N	Sunny
N1	L _{eq} 30mins	13/10/08	10:55	52.1	75	N	Sunny
N1	L _{eq} 30mins	20/10/08	14:20	52.0	75	N	Sunny
N1	L _{eq} 30mins	27/10/08	10:45	51.2	75	N	Cloudy
N2	L _{eq} 30mins	02/10/08	11:30	46.6	75	N	Sunny
N2	L _{eq} 30mins	08/10/08	13:05	51.5	75	N	Sunny
N2	L _{eq} 30mins	13/10/08	11:30	53.4	75	N	Sunny
N2	L _{eq} 30mins	20/10/08	15:00	56.7	75	N	Sunny
N2	L _{eq} 30mins	27/10/08	11:15	56.1	75	N	Cloudy
N3*	L _{eq} 30mins	02/10/08	13:00	60.7	75	N	Sunny
N3*	L _{eq} 30mins	08/10/08	13:40	53.7	75	N	Sunny
N3*	L _{eq} 30mins	13/10/08	14:15	56.6	75	N	Sunny
N3*	L _{eq} 30mins	20/10/08	13:40	48.0	75	N	Sunny
N3*	L _{eq} 30mins	27/10/08	14:13	65.6	75	N	Cloudy
N4	L _{eq} 30mins	02/10/08	13:35	55.5	75	N	Sunny
N4	L _{eq} 30mins	08/10/08	14:50	46.6	75	N	Sunny
N4	L _{eq} 30mins	13/10/08	14:50	62.9	75	N	Sunny
N4	L _{eq} 30mins	20/10/08	13:10	60.3	75	N	Sunny
N4	L _{eq} 30mins	27/10/08	14:45	49.4	75	N	Cloudy

Remarks: Raw datasheet for noise monitoring are attached in appendix D for reference.

Remark*: The equivalent noise level of N3 is corrected by +3 dB from the raw data result due to the fact that free field measurement was carried out in the location.

4.5 Action and Limit level for Construction noise

The Action and Limit (A/L) levels for construction noise are defined in Table 4.5.1. Should non-compliance of the criteria occur, action in accordance with the Action Plan in Table 4.5.2 should be carried out.

There were no recorded exceedance in the reporting month.

Table 4.5.1 Action and Limit Levels for Construction noise		
Time Period	Action Level	Limit Level
0700 – 1900 hours on normal weekdays	When one documented complaint is received	75dB(A)
Remarks: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.		

Table 4.5.2 Event / Action Plan for Construction Noise

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IC(E), ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IC(E); 2. Implement Noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E), ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

4.6 Noise Mitigation Measures

The following mitigation measures were observed from the weekly site inspection in the reporting month:

- Use of quiet powered mechanical equipment (PME)
- Implementation of the following good site practices:
 - Only well-maintained and regularly serviced plant should be operated on site
 - Silencers or mufflers on construction equipment
 - Mobile plant, if any, should be sited as far from NSRs as possible;
 - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;

5. Water Monitoring

5.1 Water Quality Monitoring Parameters and methodology

Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Turbidity, DO was measured in-situ while water samples were delivered to Accredited HOKLAS Laboratory for analysis of SS.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site were recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring location. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading would be discarded and further reading would be taken.

5.2 Monitoring Equipment

Turbidity, DO, Salinity, pH and temperature was measured by an instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

5.3 Monitoring Locations

Seven locations included a control station in upstream of each stream/ river, a monitoring station at the end of each stream/ river of the works area and a monitoring station at Silver River were proposed for the impact water quality monitoring. Water samples were collected at mid-depth of each proposed monitoring stations for measurements as well as sample collection. The Location Plan is shown in Figure 5.3.1 for reference. It is found that there were variation of monitoring location C1 and C3, where were differing from the original location proposed, due to the error of identification. But it is believed that no river works have been carried out yet the results measured in the varied locations are still valid. After the late of October, amendment has been made for the above varied locations. Water monitoring will be continued in the correct locations proposed in EM&A manual.

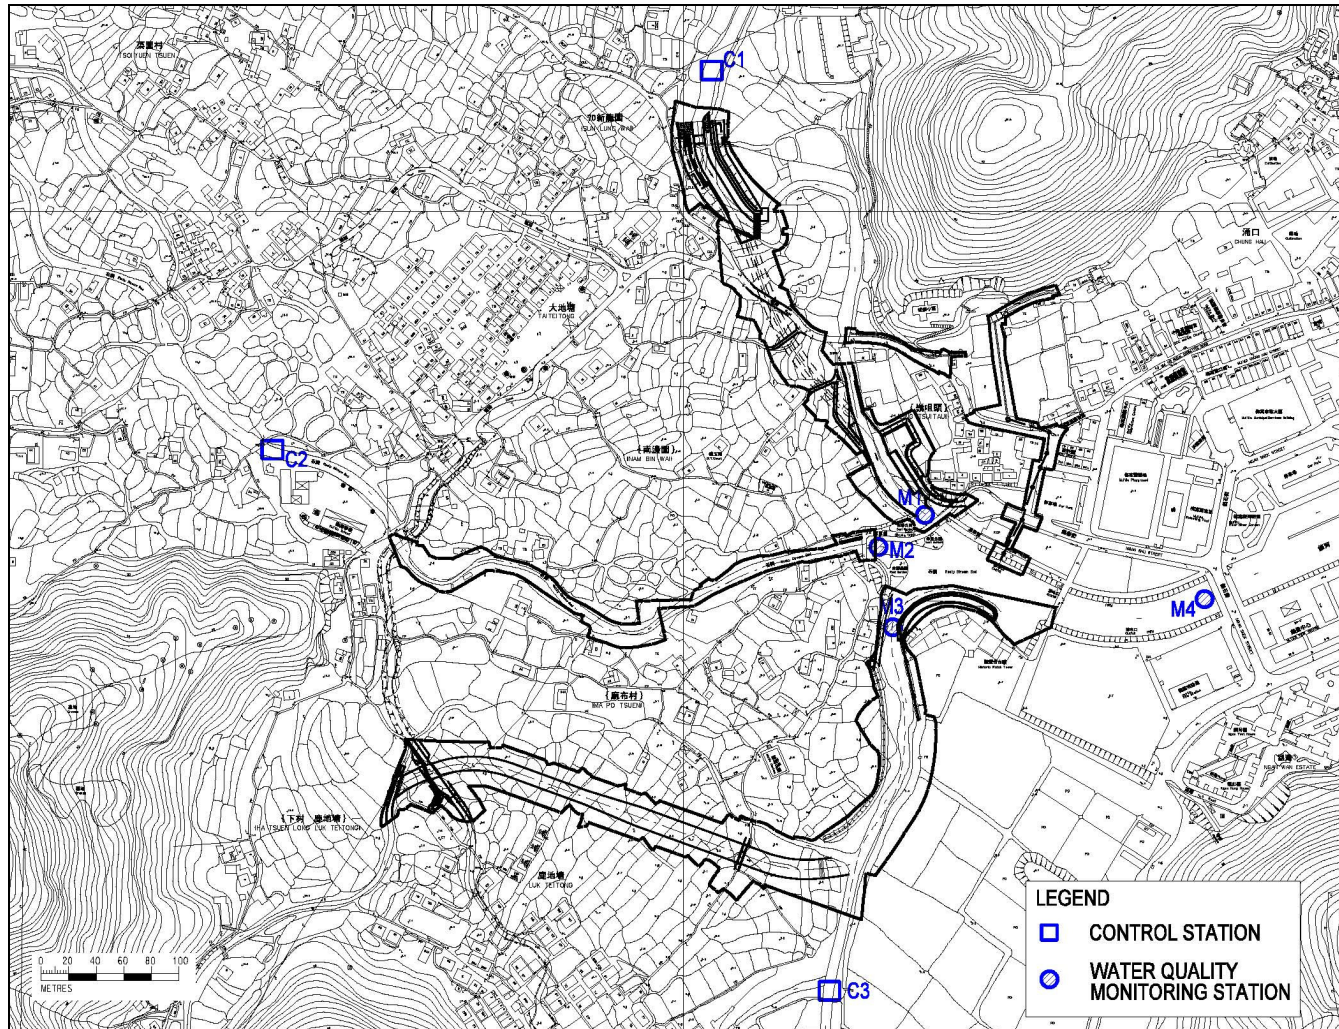


Figure 5.3.1 Water Quality Monitoring Locations

5.4 Monitoring Frequency

Impact water quality monitoring was undertaken three days per week and at ebb tides during the course of the construction river works. Upon the completion of the construction works, the monitoring exercises at the designated monitoring stations will be continued for four weeks in the same manner as the impact monitoring.

5.5 Monitoring Results and Interpretation

Water quality monitoring was carried out fourteen times during October. Detailed on-site measurements and laboratory analysis reports including QA/QC results are shown in appendix E1 and E2 respectively, while Table 5.5.1 presents consolidated results throughout the reporting month.

There were 6 exceedance events reported in 5 days, which are described as follows:

For the S.S., 1 event of exceeding the action level was reported in Location M3 (12.9mg/L), on 17/10.

For the Turbidity, 1 event of exceeding the action level was reported in Location M2 (6.0 NTU), on 24/10.

For the D.O., 4 events of exceeding the action level were reported in Location M4, on 4 days including 22/10 (5.6mg/L), 24/10 (4.3mg/L), 29/10 (5.5mg/L) and 31/10 (5.4mg/L)

For the above events, Contractor has been informed individually once the measurement results were known, ET has also studied that there were no river construction works commenced in the reporting period along the project area. The exceedances are believed that were resulted from natural seasonal change, or from the vicinity of the resident.

Table 5.5.1 Water quality monitoring results in September 2008

	M1			M2			M3			M4		
	MIN	MAX	Ave.	MIN	MAX	Ave.	MIN	MAX	Ave.	MIN	MAX	Ave
Turbidity (NTU)	0.0	6.4	3.0	0.0	6.0	1.8	0.3	13.4	8.6	2.4	13.7	8.5
DO (mg/l)	7.8	9.1	8.5	7.7	9.0	8.1	6.4	8.6	7.5	4.3	8.5	6.6
Suspended Solid (mg/l)	1.8	5.5	3.5	1.0	2.6	1.6	8.9	13.8	10.9	4.4	14.0	9.6

	C1			C2			C3		
	MIN	MAX	Ave	MIN	MAX	Ave	MIN	MAX	Ave
Turbidity (NTU)	0.0	5.5	1.9	0.0	3.4	0.7	0.0	17.0	5.4
DO (mg/l)	4.8	8.1	7.5	7.5	8.4	7.8	2.8	7.8	4.5
Suspended Solid (mg/l)	1.0	1.8	1.3	1.0	1.3	1.0	1.5	11.2	4.4

* Remarks: Detection limit for Turbidity, DO and SS are 1 NTU, 0.1 mg/L and 1 mg/L respectively.

5.6 Action and limit level for Water Quality

Based on the baseline water quality monitoring data obtained, the A/L levels are shown in Table 5.6.1. If the water quality monitoring results at any impact stations exceeded the criteria, the actions in accordance with the Event and Action Plan in Table 5.6.2 should be taken.

There are follow up actions carried out due to the exceedance events recorded from Section 5.5, contractor was informed once measurement results were known although river construction works has not been commenced.

Table 5.6.1 Action and Limit Levels for water quality monitoring

Parameters	Monitoring locations							
	M1		M2		M3		M4	
	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level
Turbidity (NTU)	15.2	16.9	5.3	6.5	16.8	26.0	16.2	18.0
DO (mg/L)	5.7	4.0	6.2	4.0	5.9	4.0	5.9	4.0
SS (mg/L)	12.2	12.8	3.1	4.2	12.4	17.7	13.9	15.2

Remarks:

For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits

For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table 5.6.2 Event and action Plan for Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level being exceed by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 2. Inform IC(E) and Contractor; 3. Check monitoring data, all plant, equipment and Contractor's working methods; 4. Discuss mitigation measures with IC(E) and Contractor; 6. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.
Action level being exceed by more than two consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; prepare to increase the monitoring frequency to daily 7. Repeat measurement on next day of exceedance 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER within three working days; 6. Implement the agreed mitigation measures.
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.

5.7 Water Quality Mitigation Measures

Construction Run-off and Drainage

The site practices outlined in ProPECC PN 1/94 ‘Construction Site Drainage’ should be followed as far as practicable during both construction and operation phase of the drainage improvement works in order to minimize surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge.

As recommended in the final EM&A manual, attention would be paid specially construction run-off and drainage, general construction activities, sewage discharged from construction workforce and river channel excavation works.

From the current observation, contractor was installing the wheel washing facilities and desilting tank as implementation of water quality mitigation measures. It is reported that those facilities will be functioned once river construction works start.

5.8 Water Monitoring Schedule for the Next reporting period

Water monitoring in the next reporting period is scheduled for 3, 6, 7, 10, 12, 14, 17, 19, 21, 24, 26 and 28 November

6. Ecology Monitoring

6.1 Ecological Monitoring Parameters

According to the Final EM&A Manual, a specific ecological monitoring programme of the improved section of PNH and LTT Rivers is recommended. The monitoring parameters required to measure in this project and survey methodology are described below:

(1) Avifauna species and abundance: Birds will be surveyed quantitatively using transect count method. Birds within the river channel and on the riverbank will be identified and their abundance will be recorded.

(2) Aquatic macroinvertebrate community species composition and abundance: Survey on aquatic fauna will focus on determination of the diversity and abundance of stream aquatic communities. Sampling methods, such as active searching, direct observation, netting, and kick sampling, will be determined according to the site conditions during field survey.

(3) Fish community species composition and abundance: Sampling methods, such as active searching, direct observation, and hand netting, will be determined according to the site conditions during field survey.

(4) Adult odonate community species composition and abundance: Adult dragonfly will be surveyed quantitatively using transect count method. Adult dragonflies within the river channel and on the riverbank will be identified and their abundance will be recorded. Species requiring close examination will be netted.

(5) Aquatic, emergent and riparian vegetation community species composition and abundance: The area will be walked through. Plant species composition and their relative abundance will be recorded.

(6) Surveys of White-shouldered Starling *Sturnus sinensis* will be conducted at the disused watchtowers next to LTT river. Breeding of the White-shouldered Starlings will be determined by checking signs of attempt to breed or sign of breeding which include carrying nesting materials, to-and-fro movement of adults carrying food, presence of recently fledged juveniles, etc. The number of breeding pairs and the site observation will be recorded whenever possible.

Water Quality Monitoring along LTT and PNH River as well as LTT bypass channel was carried out. Water quality monitoring will include Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Moreover, additional water monitoring parameters will be taken for the purposes of ecological monitoring of water quality in this project. The added information will include: BOD, Ammonia, Nitrate and Phosphate concentrations. Turbidity, DO, pH and water flow will be measured in-situ while water samples will be delivered to Accredited HOKLAS Laboratory accredited laboratory and the analyses followed the standard methods according to APHA Standard Methods for the Examination of Water and Wastewater, 20th Edition, or equivalent for analysis of SS, BOD, Ammonia, Nitrate and Phosphate concentrations.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site will be recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading will be discarded and further reading will be taken.

6.2 Monitoring Equipment and Methodology

Turbidity, DO, Salinity, pH and Temperature will be measured by a instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the

monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

6.3 Monitoring Locations

According to the Final EM&A Manual, the improved section of the river channels will be divided into 50m long sections, and ecological survey will be carried out in each of the 50m sections. A total of nine sections will be divided for the two rivers which include:

- Two sections for existing upstream of PNH river (i.e. the proposed 80m long trapezoidal channel)
- Two sections for existing downstream of PNH river (i.e. the proposed 100m long rectangular channel)
- Five sections for existing Luk Tei Tong River (i.e. the proposed 240m long trapezoidal channel)

The disused watchtowers is located at the confluence of the three rivers and next to LTT river.

The Location Plan for ecological is shown in Figure 6.1 for reference.

The improved sections of the river channels require to carrying out water quality monitoring for the ecological purpose. The sampling points for impact monitoring was undertaken in the same place as the baseline monitoring proposed, where include:

- Three points for existing of PNH river
- Three points for existing of Luk Tei Tong River

The Location Plan for ecological water monitoring is shown in Figure 6.2 for reference.

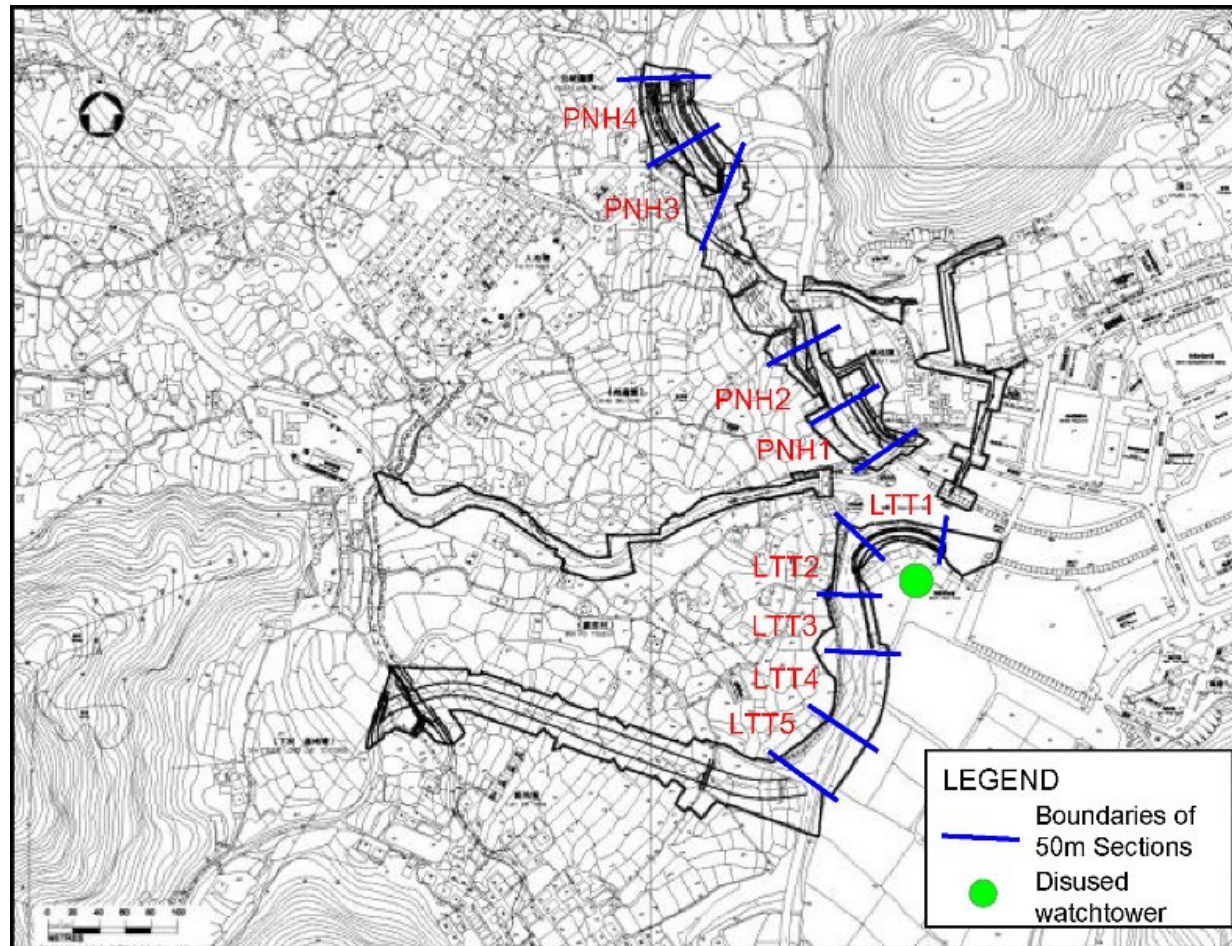


Figure 6.1 Ecological Monitoring Locations

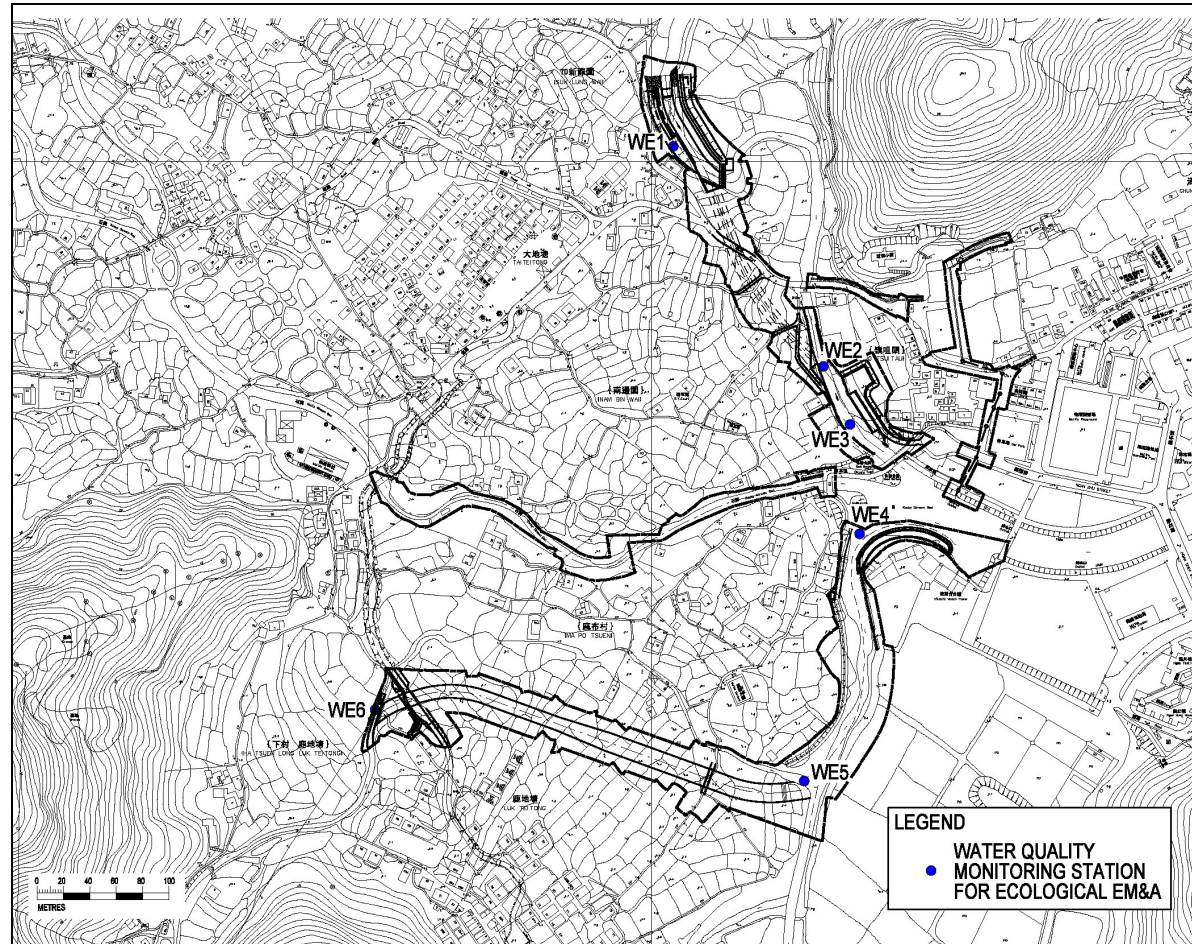


Figure 6.2 Ecological Water Quality monitoring locations

6.4 Monitoring Frequency

As proposed, impact ecological monitoring was carried out once for each monitoring location in the reporting month.

6.5 Monitoring results

Pak Ngan Heung Stream N and S sections

Vegetation

Surveys were conducted on 22 October 2008. The north section of Pak Ngan Heung Stream was fairly modified. Part of the west bank was lined with rock gabion bank and occupied by village houses and abandoned agricultural field. The stream channel was wider than the downstream section, but the stream bank was still fairly narrow and steep in gradient. Compared to the south section, the north section was relatively shaded due to presence of more trees with larger canopy.

The walk through survey recorded a total of 57 species, including 19 trees, 10 shrub, 13 herb and 6 grass species (Appendix C1). 44 of the species recorded are natives, while 13 were exotics. The quantitative sampling recorded 22 species at the north section. Large native (e.g. *Celtis sinensis*, *Cleistocalyx operculata*, *Ficus hispida*) and exotic trees (*Acacia confusa*) dominated the transects. Other species recorded include common and typical native pioneer forest and streamside tree species and ruderal species. No species of conservation interest was recorded.

Table 6.5.1 Relative percentage cover of vegetation recorded at Pak Ngan Heung (N) Section

Species	Relative % cover	
	PNH3	PNH4
<i>Acacia confusa</i>		13.9
<i>Acorus graminifolius</i>		0.8
<i>Alocasia macrorrhiza</i>		0.1
<i>Aporosa dioica</i>	4.1	2.7
<i>Bamboo</i>	12.0	
<i>Celtis sinensis</i>	24.4	25.0
<i>Christella parasitca</i>	3.5	0.5
<i>Cleistocalyx operculata</i>	13.3	
<i>Desmos chinensis</i>	3.1	
<i>Embelia ribes</i>		0.4
<i>Ficus hispida</i>		22.8
<i>Liriope spicata</i>		0.6
<i>Litsea glutinosa</i>		7.7
<i>Macaranga tanarius</i>		11.0
<i>Mallotus paniculatus</i>	17.8	
<i>Microstegium ciliatum</i>		5.5
<i>Mikania micrantha</i>		2.0
<i>Phyllanthus urinaria</i>	0.7	
<i>Pueraria phaseoloides</i>	1.5	3.5
<i>Sageretia thea</i>		3.5
<i>Sterculia lanceolata</i>	0.9	
<i>Syzygium jambos</i>	18.7	
Total Relative % Cover	100	100
Total Transect Length (m)	13.0	34

The south section of Pak Ngan Heung Stream was highly modified. Both banks were lined with rock gabions and were occupied by village houses immediately beyond the channel. The stream channel was lack of riparian zone and vegetation. A total of 21 species recorded, 16 of which were native and 5 were exotic. It was composed of isolated individuals of mangrove

(*Kandelia obovata*), backshore species (*Clerodendrum inerme*), native (*Celtis sinensis*) and planted trees (*Acacia confusa*) (Appendix C2). No species of conservation interest was recorded.

Terrestrial Fauna

Surveys were conducted on 16 October 2008.

A total of six species of birds were recorded in the proposed work area of the Pak Ngan Heung River (Table 6.5.2). All are common in Hong Kong.

Table 6.5.2 Avifauna in Pak Ngan Heung

Common names	Latin names	PNH 1	PNH 2	PNH 3	PNH 4	Commonness & distribution
Little Egret	<i>Egretta garzetta</i>	1				CW
Common Kingfisher	<i>Alcedo atthis</i>	1				CW
Grey Wagtail	<i>Motacilla cinerea</i>		1			CW
Chinese Bulbul	<i>Pycnonotus sinensis</i>			2	3	CW
Crested Bulbul	<i>Pycnonotus jocosus</i>			2	2	CW
Oriental Magpie Robin	<i>Copsychus saularis</i>			1		CW

CW = common and widespread, CL = common/uncommon and localized

Eight species of dragonfly were recorded in the proposed work area of the Pak Ngan Heung River (Table 6.5.3). All are very common in Hong Kong.

Table 6.5.3 Dragonfly in Pak Ngan Heung

Common names	Latin names	PNH 1	PNH 2	PNH 3	PNH 4	Commonness & distribution
Common Blue Jewel	<i>Rhinocypha perforata</i>			2	2	A
Black-banded Gossamerwing	<i>Euphaea decorata</i>			1		A

Lesser Emperor	<i>Anax perthenope</i>				1	C
Green Skimmer	<i>Orthetrum sabina</i>	1	1			A
Common Red Skimmer	<i>Orthetrum pruinosum</i>	2		2	3	A
Wandering Glider	<i>Pantala flavescens</i>		1	13	1	A
Crimson Darter	<i>Crocothemis servilia</i>		2			A
Indigo Dropwing	<i>Trithemis festiva</i>		2			A

A = abundant

Aquatic fauna and fish

12 species of fish (including the newly recorded Brokenband Hillstream Loach in upstream location) and four crustacean were recorded in the 4 sections at PNH. All are common and widespread in Hong Kong. Though Predaceous Chub was observed, the another one fish species of conservation concern reported in the EIA report, i.e. Flagtail Kuhlia marginata, was not recorded in PNH during the present monthly monitoring survey.

Table 6.5.4 Aquatic Invertebrates and fish in Pak Ngan Heung

Common names	Scientific names	PNH 1	PNH 2	PNH3	PNH4
Atyid shrimp	<i>Caridina elongata</i>			++	+++
Palaemond shrimp	<i>Macrobrachium hainanensis</i>	+	+	+++	++
Crab	<i>Varuna litterata</i>	++	++	+	++
Mitten Crab	<i>Eriocheir japonica</i>	++	++	+	++
Mosquito fish	<i>Gamusia affinis</i>				+
Barcheek Goby	<i>Rhinogobius giurinus</i>		+		+
Goby	<i>Rhinogobius duospilus</i>		+		++
Swordtail	<i>Xiphophorus hellerii</i>			+	++
Six-banded Barb	<i>Puntius semifasciolatus</i>				++
Unidentified Cichlid fish					++
Tilapia		++	+++	+	

Predaceous Chub	<i>Parazacco spilurus</i>		+	++	+
Jarbug Terapon	<i>Terapon jarbug</i>	++	++		
Common Silver-biddy	<i>Gerres oyena</i>	++	++		
Mullet	<i>Mugil cephalus</i>	++	++		
Broken-band Hillstream Loach	<i>Liniparhomaloptera disparis</i>				+

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Luk Tei Tong Stream Section

Vegetation

Surveys were conducted on 22 October 2008. The Luk Tei Tong Stream Section was highly modified. The stream bank from Section 1 to 4 were largely lined with rock gabions or concrete while stream bank of section 5 were fully lined with wired rock gabions and was little vegetated. Vegetation only established on isolated muddy patches at the estuary and remaining semi-natural bank which was fairly narrow and steep in gradient. The whole section appeared to be subject to tidal influence, as mangrove associated or backshore species were recorded along the whole channel.

The walk through survey recorded a total of 38 species, including 12 tree, 7 shrub, 2 herb and 7 grass species (Appendix C3). 31 of the species recorded are natives, while 7 were exotics. The quantitative sampling recorded 19 species at the middle section. Section 2 was dominated by *Terminalia catappa* and *Wollastonia biflora*, while Section 3 and 4 was dominated by *Hibiscus tiliaceus* and *Clerodendrum inerme* respectively.

Due to the patchiness of streamside vegetation, the quantitative data should be interpreted with cautions and used as a reference only.

Table 6.5.5 Relative percentage cover of vegetation recorded at Luk Tei Tong Stream Section

Species	Relative % cover		
	LLT2	LLT3	LLT4
<i>Acanthus ilicifolius</i>	42.2	15.7	4.3
<i>Artemesia sp.</i>			6.5
<i>Celtis sinensis</i>	3.8		
<i>Clerodendrum inerme</i>			27.1
<i>Dendrotrophe frutescens</i>			7.3
<i>Excoecaria agalocha</i>	5.2		0.5
<i>Fimbristylis ferruginea</i>			27.5
<i>Fimbristylis sp.</i>	3.3		
<i>Hibiscus tiliaceus</i>		69.8	1.0
<i>Ischaemum sp.</i>			7.1
<i>Kandelia obovata</i>	2.2	14.5	
<i>Papalum paspaloides</i>	7.9		1.8
<i>Phragmites karka</i>			7.8
<i>Premna serrifolia</i>	4.6		
<i>Pueraria phaseoloides</i>			7.5
<i>Scoparia dulcis</i>			1.5
<i>Terminalia catappa</i>	17.8		
<i>Toxocarpus wightianum</i>	0.2		
<i>Wollastonia biflora</i>	12.8		
Total Relative % Cover	100.0	100.0	100.0
Total Transect Length (m)	11.0	16.0	22.0

Terrestrial Fauna

The proposed work area of Luk Tei Tong River was divided into 5 sections. All recorded avifauna and dragonfly species are common in Hong Kong

Surveys were conducted on 16 October 2008.

A total of ten species of birds were recorded in these sections (Table 6.5.6). All these species are common and widely distributed in Hong Kong.

Table 6.5.6 Avifauna in Luk Tei Tong River

Common names	Latin names	LTT 1	LTT 2	LTT 3	LTT 4	LTT 5	Commonness & distribution
Little Egret	<i>Egretta garzetta</i>	1		1			CW
Common Sandpiper	<i>Actitis hypoleucos</i>	1					CW
Spotted Dove	<i>Streptopelia chinensis</i>		1				CW
Chinese Bulbul	<i>Pycnonotus sinensis</i>				3	2	CW
Crested Bulbul	<i>Pycnonotus jocosus</i>				4	2	CW
Oriental Magpie Robin	<i>Copsychus saularis</i>			1		1	CW
Masked Laughingthrush	<i>Garrulax perspicillatus</i>				2		CW
Common Tailorbird	<i>Orthotomus sutorius</i>					2	CW
Yellow-bellied Prinia	<i>Prinia flaviventris</i>				1	1	CW
Japanese White-eye	<i>Zosterops japonica</i>			2	3	4	CW

CW = common and widespread, CL = common/uncommon and localised

Five species of dragonfly were recorded in the Luk Tei Tong River (Table 6.5.7). All these species are common in Hong Kong.

Table 6.5.7 Dragonfly in Luk Tei Tong River

Common names	Latin names	LTT 1	LTT 2	LTT 3	LTT 4	LTT 5	Commonness & distribution
Common Red Skimmer	<i>Orthetrum chrysis</i>				2	1	A
Common Blue Skimmer	<i>Orthetrum glaucum</i>			1	1	2	A
Green Skimmer	<i>Orthetrum sabina</i>	2			1	1	C
Wandering Glider	<i>Pantala flavescens</i>	9					A
Crimson Dropwing	<i>Trithemis aurora</i>				2	2	A

A = abundant, C = common

Aquatic invertebrates and fish

5 species of fish, 5 species of crustacean and 2 species of mollusks were recorded in the 5 sections at LTT. All are common and widespread in Hong Kong. The two fish species of conservation concern reported in the EIA report, i.e. Flagtail *Kuhlia marginata* and Predaceous Chub *Parazacco spilurus* were not recorded in LTT during the baseline monitoring survey.

Table 6.5.8 Aquatic invertebrates and fish in Luk Tei Tong River

Common names	Scientific names	LTT1	LTT2	LTT3	LTT4	LTT5
Mangrove clam	<i>Geloina erosa</i>			+	+	
Snail	<i>Melanoides tuberculata</i>	++	++	+++	+++	+
Crab	<i>Varuna litterata</i>	++	++	+	+	+
Fiddler crab	<i>Uca lactea</i>		++	+++		
Fiddler crab	<i>Uca arcuata</i>	++	++			
Fiddler crab	<i>Uca crassipes</i>		+	+		
Crab	<i>Perisesarma bidens</i>		+	+	++	+++
Common mudskipper	<i>Periophthalmus cantonensis</i>	++	++	++	+	
Tilapia		++	++	+		
Jarboa terapon	<i>Terapon jarbua</i>	++	+	+		
Mullet	<i>Mugil cephalus</i>	+++	++			
Common Silver-biddy	<i>Gerres oyena</i>	++				

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Discussed Watchtowers

Surveys were conducted on 16 October 2008.

There was no sign (e.g., adults carrying food or nesting materials) of use of the watchtower as nesting habitat by White-shouldered Starling.

No bird entered the tower during the evening survey. Rather, flocks of tens

of Crested Mynas *Acridotheres cristatellus*, a bird species belonging to same family of White-shouldered Starling, roosts on casuarina trees near the watchtower during the survey session in evening. It seems the birds do not prefer the watchtower as night roost.

Ecological Water Quality Monitoring (EWQM)

EWQM was conducted on 9 October 2008. Monitoring results are summarized in table 6.9. Detailed on-site measurements and laboratory report are presented in appendix C4 and C5.

To review the results in table 6.5.9 in general, Suspended Solid (11.75 mg/l) turbidity (7.60 NTU) and salinity (4.4 ppt) recorded in location WE4 is higher than that of the others. However, they are close to the results recorded in the baseline monitoring report, shown as suspended solid (3.0 mg/l), turbidity (6.96 NTU) and salinity (7.6 ppt).

Table 6.9 Summarized Ecological water quality monitoring results (5 September 2008)

Parameters	Limit of detection	WE1	WE2	WE3	WE4	WE5	WE6
Suspended Solid (mg/l)	1	1.45	2.20	2.90	11.75	6.75	1.90
Nitrogen (Ammonia) (mg/l)	0.01	0.42	0.39	0.19	0.35	0.52	0.22
Nitrogen (Nitrate) (mg/l)	0.01	0.09	0.13	0.15	0.39	0.12	0.10
Phosphorous (mg/l)	0.01	0.03	0.03	0.03	0.07	0.17	0.02
BOD ₅ (mg/l)	1	1	2	1	2	2	< 1
DO (mg/l)	0.01	7.74	8.27	8.76	7.78	8.43	8.13
Turbidity (NTU)	0.01	0.45	1.15	3.35	7.60	4.65	0.00
Temperature (oC)	0.1	25.9	26.8	26.4	28.5	29.6	26.2
pH	0.01	6.44	6.61	7.31	6.67	7.07	6.80
Salinity (ppt)	0.1	0	0	0.4	4.4	0.5	0
Conductivity (ms/m)	0.1	4.4	13.3	77.3	77.0	95.2	4.8
Water Flow (m/s)	N/A	0.8	0.4	0.4	0.2	0.3	0.5

6.6 Action and Limit level for Monitoring of White-shouldered Starlings

A simple Event and Action Plan is shown in Table 6.6.1. Should the Event occur, action in accordance with the Action Plan should be carried out.

There was no recorded event in the reporting month.

Table 6.6.1 Event / Action Plan for Monitoring of White-shouldered Starlings

EVENT	ACTION	
	ET Leader	Contractor
Identification of disturbance to breeding White-shouldered Starlings	1. Increase frequency of monitoring to twice weekly	1. Check all construction actions and working methods
	2. Notify Site Engineer	2. Submit proposals for remedial action to prevent abandonment of the breeding site.
	3. Review construction activities of previous week.	3. Implement remedial action.
	4. Identify any changes in construction activities in previous week	4. Liaise with ET regarding effectiveness of remedial actions.
	5. Discuss remedial actions with Site Engineer	

6.7 Ecological monitoring Schedule

The next Ecological water monitoring date is set on 11th of November, while the next ecological monitoring dates are set on 11th, 15th and 21st of November.

7. Action taken in Event of Exceedence

If the measurements (Noise, Water, Ecology) exceed the action / limit level, exceedance details will be reported and follow-up actions will be taken by relevant parties involved.

During the reporting period:

- No exceedance was recorded for construction noise.
- 6 exceedance events were recorded for the water quality monitoring.
However there is no river construction works has been commenced yet.
- No exceedance was recorded for ecological monitoring.

There was no exceedance for noise, water quality and ecological measurements that is directly caused by the project recorded during this reporting period; therefore no actions were taken.

8. Construction waste disposal

It is the contractor's responsibility to ensure that all wastes produced during the construction phase for the drainage improvement works are handled, stored and disposed of in accordance with good waste management practices and EPD's regulation and requirement. Waste materials generated during construction activities, such as construction and demolition (C&D) material, chemical wastes and general refuse, are recommended to be audited at regular intervals to ensure that proper storage, transportation and disposal practices are being implemented.

Contractor has completed the registration of Waste Producer under the Waste Disposal (Chemical Waste)(General) Regulation. The Waste Producer Number, WPN 5213-950-Y2443-03 was assigned by EPD on 12 Aug 2008. The Contractor would be responsible for the implementation of any mitigation measure to minimize waste or redress problems arising from the waste materials.

Table 8.1 is a summary of updated figures of the construction wastes disposal provided by the Contractor.

Table 8.1 Summary of Construction Waste Disposal

	Amount of Construction Waste disposed		
	Inert Waste (to Public Fill)	Non-inert Waste (to Landfill)	Chemical Waste (to treatment plant)
1 st October 08 to 31 st October 08	2056 (ton)	0	0
1 st September 08 to 30 th September 08	15.22 (ton)	0	0
18 th August 08 to 31 st August 08	0	0	0
2 nd July 08 to 31 st July 08	21.33 (ton)	0	0
2 nd June 08 to 30 th June 08	56.83 (ton)	0	0

9. Status of Permits and Licenses obtained

Table 9.1 is the updated status of environmental related permits/ license obtained for the construction activities

Table 9 .1 Status of Permits and Licenses Obtained

Description	License / Permit No.#	Date of Issue	Date of Expiry	Remarks
Environmental Permit	EP-237/2005/A	05 Mar 2008	--	Issued
Registration of C&D Waste Producer	7006521	--	--	Issued
Chemical Waste Producer	5213-950-Y2443-03	12 Aug 2008	--	Issued
Construction Noise Permit	N/A	N/A	N/A	N/A
Effluent Discharge License	EP890/W2/XG032 EP890/W2/XG033 EP890/W2/XG034 EP890/W2/XG035 EP890/W2/XG036 EP890/W2/XG037 EP890/W2/XG038 EP890/W2/XG039 EP890/W2/XG040 EP890/W2/XG041	23 Oct 2008	31 Oct 2013	Issued

The contractor implemented various environmental mitigation measures as recommended in the Environmental Permit and Final Mitigation Measures Report. The implemented schedule is presented in appendix H.

10. Complaint Log

There was no formal complaint received during the reporting month.

	Noise	Water	Ecology	Cultural	Others
Sept 2008	0	0	0	0	0
Total	0	0	0	0	0

11. Site Environmental Audits

11.1 Site Inspection

With an intention to ensure that appropriate environmental protection and pollution control mitigation measures are properly implemented, regular environmental site inspections have been scheduled.

Within the reporting month, site inspections were conducted on 3, 10, 17, 24 and 31 of October.

A detailed checklist of each site inspection together with comments, relevant photos and maps have been filed and kept. A summary of observation and follow-up action is shown in table 11.1

Date	Observations	Advice from ET	Action taken	Closing Date
03 Oct 08	Stagnant water was found at the site of PNH box culvert.	Contractor was advised to pump off those water regularly	Action taken as advised by ET	08 Oct 08
17 Oct 08	Erosion risk of the excavated materials was observed at the U-channel construction site of Ling Tsui Tau	Contractor was advised to cover the piles with tarpaulin	Action taken as advised by ET	Ongoing
17 Oct 08	General waste such as wood logs & foams were found dumping improperly at the site of PNH box culvert	Contractor was advised to assign a refuse collection area for waste storage and segregation. And reuse if possible.	Action taken as advised by ET. Reuse issues for wood logs were implemented	24 Oct 08
24 Oct 08	Dust concern generated from the surface of sites and excavated materials	Contractor was advised to provide watering for sites and piles of material more frequently	Action taken as advised by ET. Efficiency of the measures will be kept checking	Ongoing

Table 11.1 Summary of site inspection

Date	Observations	Advice from ET	Action taken	Closing Date
31 Oct 08	A mini power generator without drip tray was found occupying in the site of Ling Tsui Tau	Contractor was requested to provide a proper drip pan for the equipment immediately	To be checked	Nil
31 Oct 08	A oil drum was found placing in improper manner horizontally, and without drip pan at the site of PNH box culvert	Contractor was requested to replace the drum and provide a drip pan immediately	To be checked	Nil

11.2 Compliance with legal and Contractual requirement

ET leader has reviewed the progress and programme of the works to check that contractor has not violated relevant environmental laws.

11.3 Environmental Complaint and follow up actions

During this reporting period, there are not any complaints. Therefore, follow up actions for the Environmental Complaint is not required

12. Future key issues

Key construction activity in the coming month will be construction of box culvert at PNHR, and site clearance works at the LTT marsh. It is expected that noise impacts and waste disposal will be generated on-site, and certain ecological and water quality impacts may be resulted from site clearance works. With reference to the EM&A manual, mitigation measure report as well as the environmental permit, the following mitigation measures are proposed to be taken, if necessary.

- Adoption of movable noise barriers and temporary noise barriers.
- Application of good site practices mentioned in EM&A manual Clause 3.8.1.
- Construction wastes, such as construction and demolition (C&D) material, chemical waste and general refuse, should be managed and disposed to the designated public fill and landfill areas in acceptable manner. Wastes are recommended to be audited at regular intervals to ensure that proper storage, transportation and disposal practices are being implemented.
- Contractor has to take serious caution on the turf condition in LTT marsh during site clearance works, removal of the turf due to the construction works shall be minimized and those should be properly removed, stored, maintained and reused for lining the riverbed of Luk Tei Tong Bypass channel.

13. Conclusions

In this reporting month, land based construction work for box culvert in PNH and construction works of U-channel at Ling Tsui Tau were carried out. No river works were conducted in the project area.

Regular site meetings and inspection audits led by the seniors for discussing site environmental matters were held among Project Proponent, Contractor and the ET on weekly basis. Also monthly site meeting and inspection audits with the above parties and IEC was carried out at the late of the reporting month.

For noise level monitoring, all results were within the established A/L limits.

For water quality monitoring, majority of the recorded levels were within established A/L limits. 6 exceedance events of Turbidity, Dissolved Oxygen and Suspended Solid were reported. However there is no river construction works has been commenced yet. According to the monthly ecological water monitoring results performed on 5 Sept 2008, suspended turbidity and salinity level recorded in location WE4 was higher than that of the others. However, these are similar with the baseline monitoring results.

During ecological monitoring survey, no White-shouldered Starling was recorded breeding in the watch tower. And there was no sign of disturbance from the Project to the watch tower as no construction work of the Project were conducted near the tower in November 2008. The breeding season of White-shouldered Starling is probably over in this time of the year. In addition, no disturbance on the flora and fauna in the river channels were observed during the ecological monitoring.

Also, there were not any notifications of summons recorded during the reporting period. Furthermore, there were not any formal prosecution and complaints recorded.

Minor housekeeping deficiency such as dust, accumulated water and handling of equipments have been observed and appropriate actions have been taken by the contractor as advised. Installation of proper desilting as well as wheel washing facilities required was observed during the reporting month.

ET has reminded the contractor to provide environmental pollution control measures wherever necessary; and to keep a good environmental management at site practice.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement.
