

Drainage Service Department

Monthly Environmental Monitoring & Auditing report for

Contract No.DC/2006/11

Drainage Improvement in Southern Lantau

March 2010

Environmental Pioneers & Solutions Limited

8/F, Chaiwan Industrial Centre Building


20 Lee Chung Street, Chaiwan, Hong Kong

Tel: 2965 0828


Fax: 2856 2010

APPROVAL SHEET

Prepared and Certified by: ET Leader (Environmental Pioneers & Solutions Limited)

Signature: 
Miss Patricia Chung
(ET* Leader)

Date: 10/17/2010

Signature: 
Mr. Vincent Lai
(Ecologist)

Date: 12/7/2010

* ET – Environmental Team

TABLE of CONTENT

TABLE of CONTENT	ii
EXECUTIVE SUMMARY	iv
1. Introduction	1
2. Project Information	1
2.1 Construction program	1
2.2 Project Organization	2
2.3 Key Personal Contact information chart	2
3. Construction Stage	3
3.1 Construction Activities in the reporting month	3
3.2 Construction Activities for the coming month	3
3.3 Environmental Status	3
4. Noise Monitoring	4
4.1 Monitoring Parameters and Methodology	4
4.2 Monitoring Equipment	4
4.3 Monitoring Locations	5
4.4 Monitoring Results and Interpretation	7
4.5 Action and Limit level for Construction noise	7
4.6 Noise Mitigation Measures	9
5. Water Monitoring	10
5.1 Water Quality Monitoring Parameters and methodology	10
5.2 Monitoring Equipment	10
5.3 Monitoring Locations	11
5.4 Monitoring Frequency	13
5.5 Monitoring Results and Interpretation	13
5.6 Action and limit level for Water Quality	15
5.7 Water Quality Mitigation Measures	17
5.8 Water Monitoring Schedule for the Next reporting period	18
6. Ecology Monitoring	19
6.1 Ecological Monitoring Parameters	19
6.2 Monitoring Equipment and Methodology	20
6.3 Monitoring Locations	21
6.4 Monitoring Frequency	24
6.5 Monitoring results	24
6.6 Action and Limit level for Monitoring of White-shouldered Starlings	32

6.7	Ecological monitoring Schedule	32
7.	Action taken in Event of Exceedence	33
8.	Construction waste disposal.....	35
9.	Status of Permits and Licenses obtained.....	36
10.	Complaint Log	37
11.	Site Environmental Audits	37
11.1	Site Inspection.....	37
11.2	Compliance with legal and Contractual requirement.....	41
11.3	Environmental Complaint and follow up actions.....	41
12.	Future key issues.....	41
13.	Conclusions.....	43

APPENDIXES

Appendix A	Construction Programme and location plan
Appendix B	Key Personal Contact information chart
Appendix C	Calibration Certificates for measuring instruments
Appendix D1	Plant species recorded at Pak Ngan Heung River (N)
Appendix D2	Plant species recorded at Pak Ngan Heung River (S)
Appendix D3	Plant species recorded at Luk Tei Tong River
Appendix D4	Ecological Water Monitoring results (on-site measurement)
Appendix D5	Ecological Water Monitoring results (lab-report)
Appendix E	Construction Noise Monitoring Data Sheet
Appendix F1	Water Quality Monitoring Data Sheet
Appendix F2	Water Quality Monitoring Lab report
Appendix G	Monitoring Schedule for March 2010
Appendix H	Implementation status of environmental protection / mitigation measures
Appendix I	Graphical plot of water quality monitoring results (SS, DO, turbidity)
Appendix J	Graphical plot of noise monitoring results

EXECUTIVE SUMMARY

This is twentieth monthly environmental Monitoring and audit (EM&A) report for “Drainage Improvement in Southern Lantau Investigation”. The environmental permit number is “EP-237/2005/B”. The report concludes the impact monitoring for the activities undertaken during the period of 01 March 2010 to 31 March 2010. The major activities in this reporting month include construction of box culvert, retaining wall, gabion wall and mass concrete wall at Pak Ngan Heung (PNH) and Luk Tei Tong (LTT) River.

Noise, water quality and ecological monitoring were performed. Results obtained were checked against the previously established Action / Limit (A/L) levels. Additionally, the implementation status of environmental mitigation measures, event / action plan and environmental complaint handling procedures were inspected during weekly site environmental audit.

In general, waste management was satisfactory during the reporting month.

Impact monitoring for construction noise was conducted in the reporting period. No exceedance of A/L level was reported.

Furthermore, impact monitoring for water quality was conducted. Total 80 non-compliance events of water quality criteria were recorded in this reporting period while 30 of them were believed to be mainly attributed to improper site practice and insufficient of water quality mitigation measures on site. As such, contractor was advised to implement necessary corrective actions and mitigation measures as to stop further deterioration of water quality.

Ecological findings prepared by the Ecologist were outstanding therefore relevant information was not updated in this reporting period.

In regard to the muddy effluent discharge causing contamination to the river channel, site investigation was made by inspector from Environmental Protection Department and a yellow form was issued to the Contractor. Details of the incident please refer to Section 11.2.

Key construction activity in the coming month will include construction of box culvert, gabion wall, retaining wall and sloping seawall. It is expected that noise, air and water quality impacts will be resulted from the works. With reference to the EM&A manual and mitigation measure report, mitigation measures are proposed to be taken, if necessary.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement.

1. Introduction

This is the twentieth monthly Environmental Monitoring and Audit (EM&A) Report for “Drainage Improvement in Southern Lantau Investigation” project (Environmental Permit No. EP-237/2005/B)

2. Project Information

2.1 Construction program

The “Drainage Improvement in Southern Lantau Investigation” project will be completed by January 2011. The project comprises the following:

- Construction of approximately 80m long gabion with natural bed in Pak Ngan Heung River, approximately 180m of three cells 3m x 2m box culvert and approximately 100m of rectangular channel at Pak Ngan Heung River;
- Construction of approximately 250m of 0.75m wide U-Channel at Ling Tsui Tau Village in Mui Wo;
- Construction of bypass channel of about 350m and 240m long of gabion channels at Luk Tei Tong River respectively; and
- Widening three existing bottlenecks with gabion lined at Tai Tei Tong (TTT) River

Appendix A shows the construction program and location plan of the project.

2.2 Project organization

The Main Contractor, Yick Hing Construction Company Limited, has commissioned Environmental Pioneers & Solutions Limited and Ecosystems Limited as the Environmental Team, which comprises the environmental team leader, the ecologists and the environmental technicians to undertake the environmental monitoring and audit work for this project.

The environmental management structure and is shown in Fig 2.2.1.

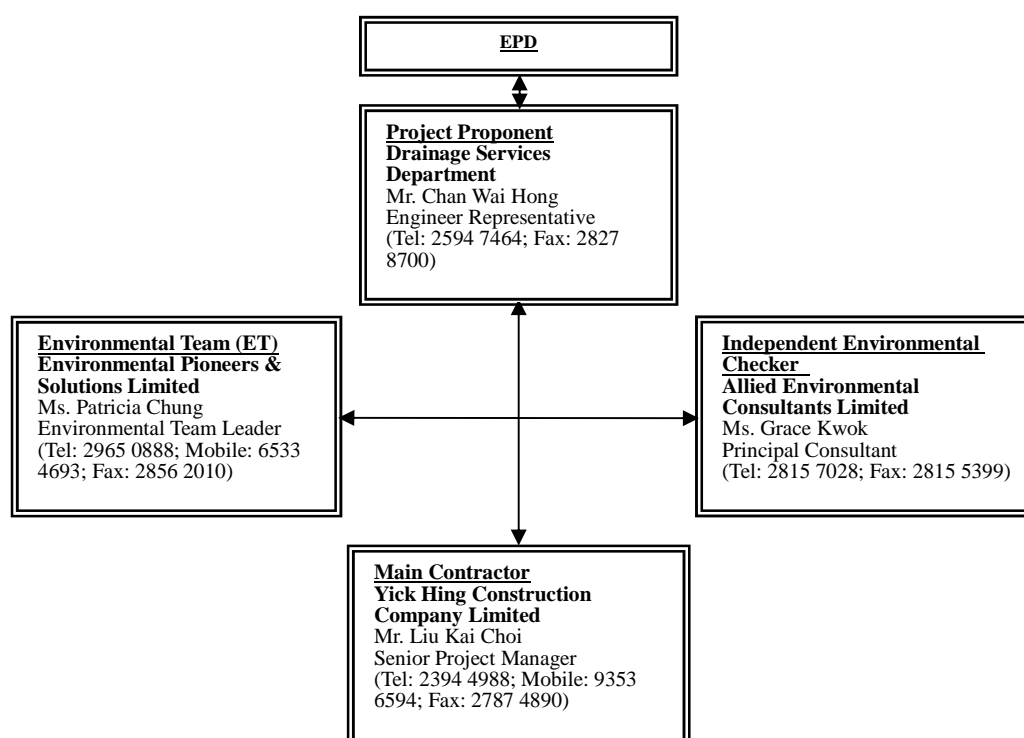


Figure. 2.2.1 Environmental Management structure for the project

2.3 Key personal contact information chart

Detailed contact of key persons involved in environmental aspect of the project is shown in Appendix B.

3. Construction Stage

3.1 Construction activities in the reporting month

Major activities in the reporting month included the followings:

1. Construction of retaining wall G at PNH River.
2. Construction of retaining walls at the upstream end of PNH River.
3. Construction of gabion wall at LTT River.
4. Construction of alternative mass concrete wall at LTT River.
5. Construction of riverwall around Yuen's Compound.
6. Construction of box culvert A and inlet at LTT bypass channel.

3.2 Construction activities for the coming month

Proposed key construction works in the coming month will include:

1. Construction of retaining wall G at PNH River.
2. Construction of retaining walls at the upstream end of PNH River.
3. Construction of fish ladder at the upstream end of PNH River.
4. Construction of gabion wall at LTT River.
5. Construction of alternative mass concrete wall at LTT River.
6. Construction of riverwall around Yuen's Compound.
7. Construction of box culvert A and inlet at LTT bypass channel.

3.3 Environmental Status

Appendix A shows the drawing of the project area.

Locations of the monitoring and control stations with environmental sensitive receivers are presented in Section 4.3, 5.3 and 6.3 for noise, water and ecological monitoring respectively.

4. Noise Monitoring

4.1 Monitoring Parameters and Methodology

The construction noise level was measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30minutes)}$ was used as the monitoring parameter for the impact monitoring in the time period between 0700 to 1900 hours on normal weekdays. For all other time period, $L_{eq(5minutes)}$ was employed for comparison with the Noise Control Ordinance (NCO) criteria.

Noise measurement results obtained from each monitoring location were recorded in the Construction Noise Monitoring Data Sheet (Appendix E) immediately after the measurement. As supplementary information for data auditing, statistical results L_{10} and L_{90} were also be recorded for reference.

In case of non-compliance with the construction noise criteria, more frequent monitoring, as specified in the Action plan in Table 4.5.2, shall be carried out. This additional monitoring shall be carried out until the recorded noise levels are rectified or proved to be irrelevant to the construction activities.

4.2 Monitoring Equipment

The sound level meters and calibrators comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum (TM) to the Noise Control Ordinance was deployed as monitoring equipment for noise measurement.

Noise measurement was not be made in the presence of fog, rain, wind with a steady speed exceeding $5ms^{-1}$ or wind with gust exceeding $10ms^{-1}$. Thus wind speed was checked by the portable wind speed indicator capable of measuring the wind speed in m/s. Table 4.2.1 summarizes the equipment list for noise monitoring

Table 4.2.1 Equipment List for Noise Monitoring

Equipment	Manufacturer & Model No.	Precision Grade	Qty
Integrated sound level meter	ACO Japan, model 6224	IEC 651 Type 1 IEC 804 Type 1	1
Windscreen	Microtech gefell model W2	N/A	1
Acoustical calibrator	Castle GA 607 B & K, model 4231	IEC 942 Type 1	1
Wind speed indicator	Kestrel K1000	N/A	1
Remarks: Calibration details for the sound level meter is given in Appendix C for reference			

4.3 Monitoring Locations

According to the Baseline Monitoring Report issued in May 2008 for the captioned project, four locations were alternative from the locations proposed in EM&A manual, were designated for baseline noise monitoring. For the data validation, impact noise monitoring was undertaken in the same locations during the construction phase of the project. The proposed monitoring locations are summarized in Table 4.3.1. Figure 4.3.1 shows the Noise Monitoring Locations

Noise measurement in each monitoring locations were taken at a point 1m from the exterior of the selected premises and at a height with no disturbance to the dweller and least obstructed view.

Table 4.3.1 Noise Monitoring Locations during Construction Phase

Identification No.	Noise Monitoring Locations
N1	No. 73, Village House, Ling Tsui Tau Tsuen (ground level)
N2	No. 31, Village House, Ling Tsui Tau Tsuen (ground level)
N3	Fence wall outside No. 5 village house adjacent to Luk Tei Tong River Outlet (ground level)
N4	No. 23, Village House, Tai Tei Tong River (ground level)

In accordance with the requirements in the EM&A manual, weekly impact monitoring was conducted. For the time period between 0700 and 1900 hours on normal weekdays, and noise parameter of $L_{eq(30minutes)}$ was measured. As if the construction works were carried out during restricted period (ie. 1900-2300, 2300-0700 of next day and Sundays / general holiday), impact monitoring that comprises 3 consecutive $L_{eq(5minutes)}$ would be carried out.

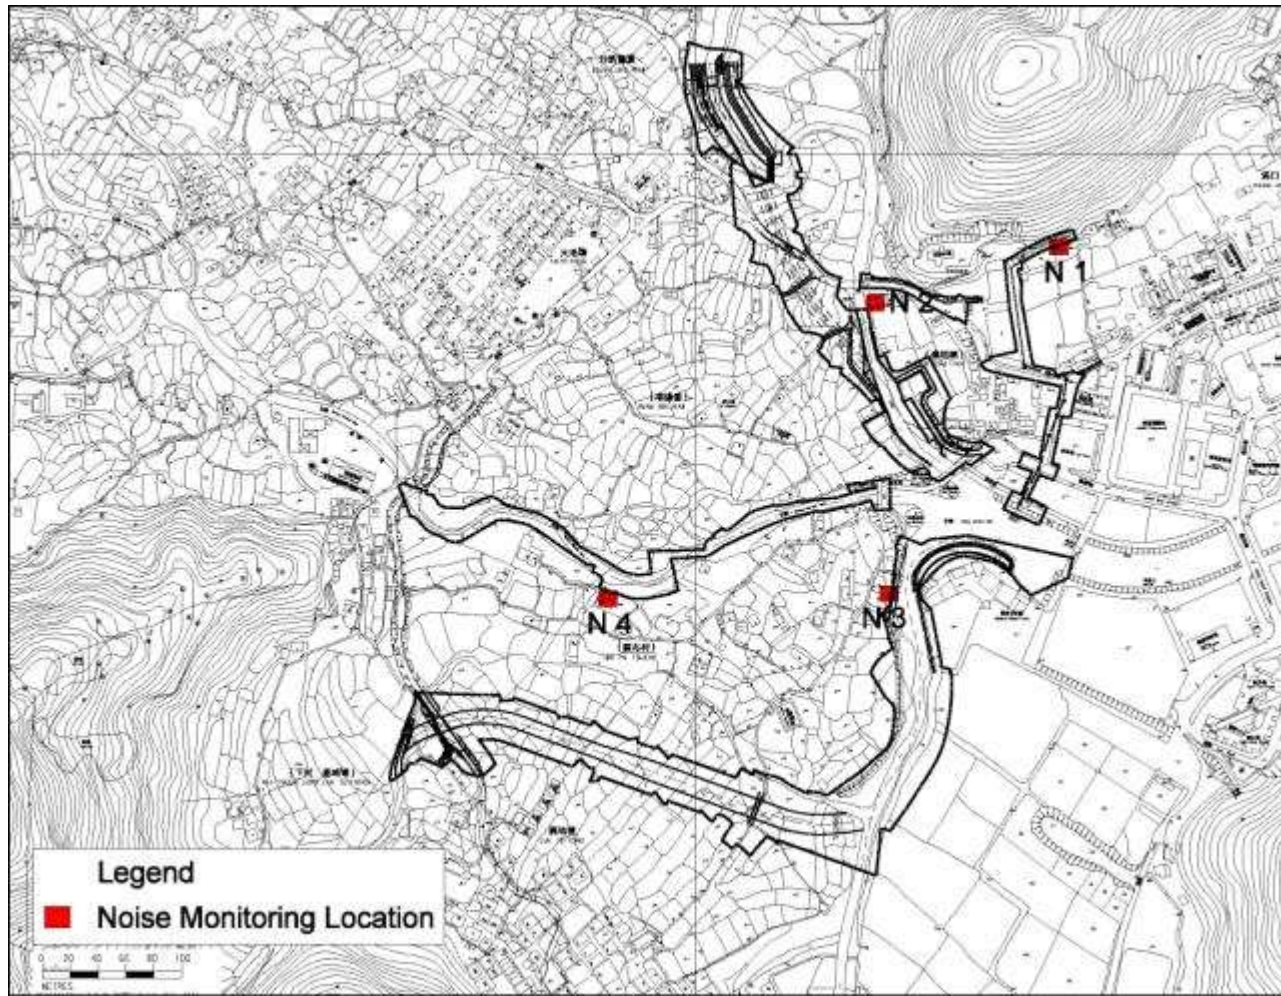


Figure 4.3.1 Impact noise monitoring locations

4.4 Monitoring Results and Interpretation

Relevant details of the noise monitoring results are presented in Table 4.4.1. The results, ranged between 49.4 dB(A) and 64.7 dB(A), were within the limit levels and therefore, no exceedance was found.

Table 4.4.1 Noise monitoring results

Table 4.4.1 Noise Monitoring Results for the reporting month							
Location	Parameter	Date	Time	L _{Aeq} dB(A)	Limit dB(A)	Exceedance	Weather
N1	L _{eq} 30mins	5-Mar-10	14:20	56.9	75	N	Sunny
N1	L _{eq} 30mins	12-Mar-10	14:50	53.1	75	N	Cloudy
N1	L _{eq} 30mins	19-Mar-10	13:00	57.8	75	N	Sunny
N1	L _{eq} 30mins	26-Mar-10	14:10	57.3	75	N	Sunny
N2	L _{eq} 30mins	5-Mar-10	13:40	64.7	75	N	Sunny
N2	L _{eq} 30mins	12-Mar-10	14:15	62.1	75	N	Cloudy
N2	L _{eq} 30mins	19-Mar-10	13:35	62.3	75	N	Sunny
N2	L _{eq} 30mins	26-Mar-10	14:45	56.9	75	N	Sunny
N3*	L _{eq} 30mins	5-Mar-10	13:00	54.8	75	N	Sunny
N3*	L _{eq} 30mins	12-Mar-10	13:40	52.3	75	N	Cloudy
N3*	L _{eq} 30mins	19-Mar-10	11:55	51.6	75	N	Sunny
N3*	L _{eq} 30mins	26-Mar-10	13:35	55.3	75	N	Sunny
N4	L _{eq} 30mins	5-Mar-10	11:35	52.9	75	N	Sunny
N4	L _{eq} 30mins	12-Mar-10	13:05	49.4	75	N	Cloudy
N4	L _{eq} 30mins	19-Mar-10	11:20	51.5	75	N	Sunny
N4	L _{eq} 30mins	26-Mar-10	13:00	51.2	75	N	Sunny

Remarks: Raw datasheet for noise monitoring are attached in Appendix E for reference.

Remark*: The equivalent noise level of N3 is corrected by +3 dB from the raw data result due to the fact that free field measurement was carried out in the location.

4.5 Action and Limit level for Construction noise

The Action and Limit (A/L) levels for construction noise are defined in Table 4.5.1. Should non-compliance of the criteria occur, action in accordance with the Action Plan in Table 4.5.2 should be carried out.

There was no exceedance recorded in the reporting month.

Time Period	Action Level	Limit Level
0700 – 1900 hours on normal weekdays	When one documented complaint is received	75dB(A)
Remarks: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.		

Table 4.5.2 Event / Action Plan for Construction Noise

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IC(E), ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IC(E); 2. Implement Noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E), ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

4.6 Noise Mitigation Measures

The following mitigation measures were observed from the weekly site inspection in the reporting month:

- Use of quiet powered mechanical equipment (PME)
- Implementation of the following good site practices:
 - Only well-maintained and regularly serviced plant should be operated on site;
 - Silencers or mufflers on construction equipment;
 - Mobile plant, if any, should be sited as far from noise sensitive receivers as possible; and
 - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.

5. Water Monitoring

5.1 Water Quality Monitoring Parameters and methodology

Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Turbidity, DO was measured in-situ while water samples were delivered to Accredited HOKLAS Laboratory for analysis of SS.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site were recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring location. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading would be discarded and further reading would be taken.

5.2 Monitoring Equipment

Turbidity, DO, Salinity, pH and temperature was measured by an instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

Detailed calibration records of the multimeter were shown in Appendix C for reference.

5.3 Monitoring Locations

Seven locations included a control station in upstream of each stream/ river, a monitoring station at the end of each stream/ river of the works area and a monitoring station at Silver River were proposed for the impact water quality monitoring. Water samples were collected at mid-depth of each proposed monitoring stations for measurements and sample collection. The Location Plan is shown in Figure 5.3.1 for reference.

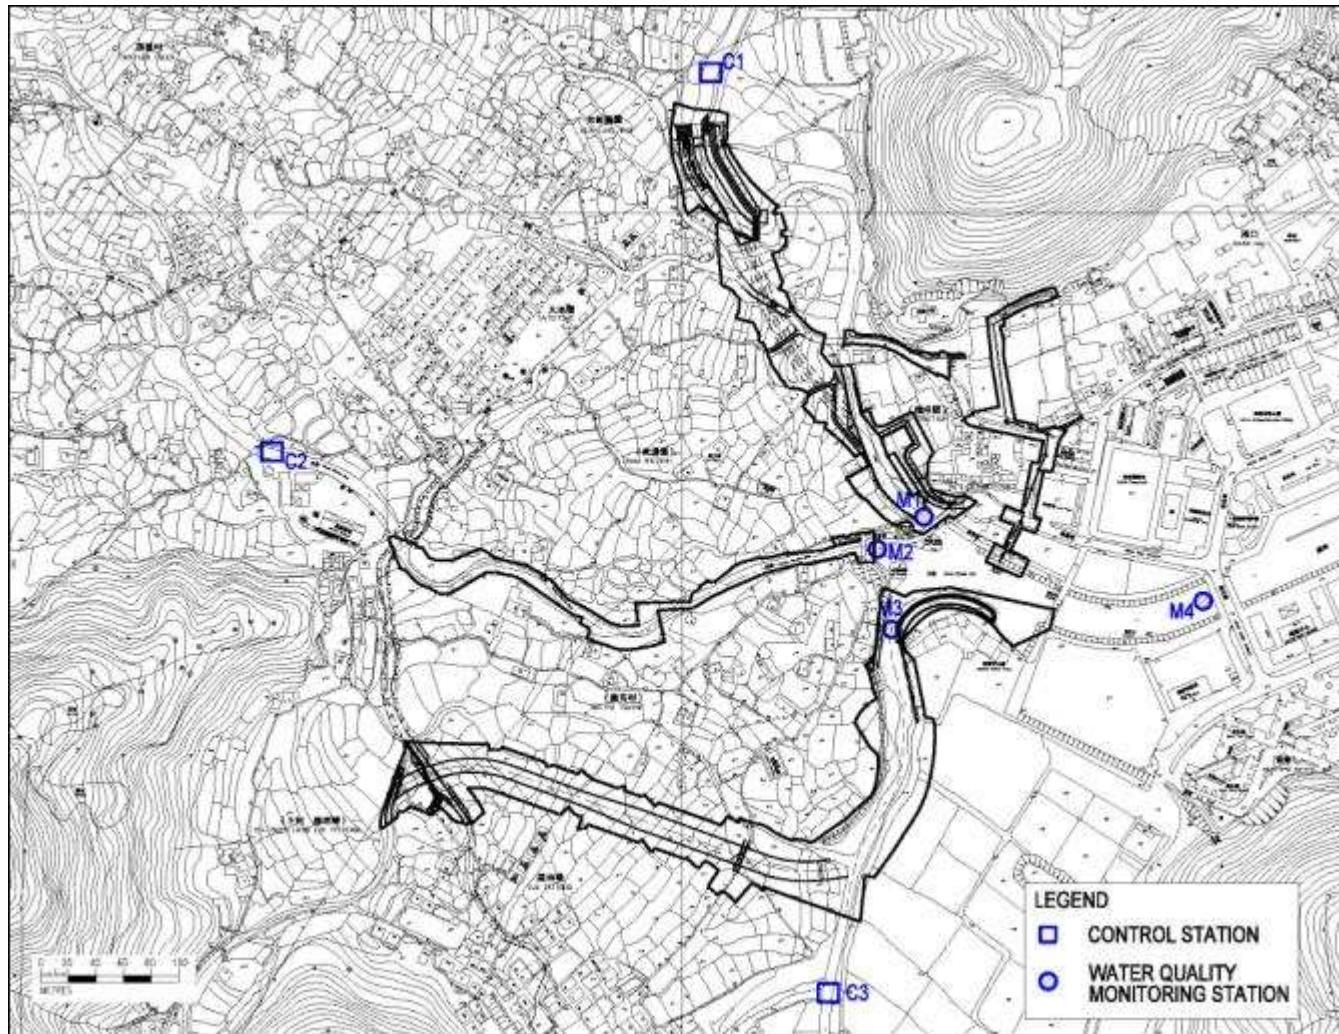


Figure 5.3.1 Water Quality Monitoring Locations

5.4 Monitoring Frequency

Impact water quality monitoring was undertaken three days per week and at ebb tides during the course of the construction river works. Upon the completion of the construction works, the monitoring exercises at the designated monitoring stations will be continued for four weeks in the same manner as the impact monitoring.

5.5 Monitoring Results and Interpretation

Water quality monitoring was carried out twenty times during March. Detailed on-site measurements and laboratory analysis reports including QA/QC results are shown in Appendix F1 and F2 respectively, while Table 5.5.1 presents consolidated results throughout the reporting month.

Total 80 exceedance events on parameters of turbidity and suspended solids were recorded in this reporting month according to the established level. Findings from the investigations showed most of the exceedance events were mainly caused by natural fluctuation and deficiencies of site practice.

As 30 events were suspected to be related to improper site practices, contractor was seriously reminded to review the site conditions and implement corrective actions as well as mitigation measures as soon as possible to minimize further deterioration of water quality.

Detailed information of the exceedance events and action taken were presented in Section 7.

Table 5.5.1 Water quality monitoring results in March 2010

	M1			M2			M3			M4		
	MIN	MAX	Ave	MIN	MAX	Ave	MIN	MAX	Ave	MIN	MAX	Ave
Turbidity (NTU)	0.0	130.7	17.1	0.0	3.2	0.5	3.3	552.6	58.2	2.5	55.8	12.8
DO (mg/l)	7.6	10.8	9.0	9.6	13.3	11.3	6.1	12.9	9.6	8.1	12.1	9.8
Suspended Solid (mg/l)	2.9	116.2	16.8	1.1	2.9	1.9	8.6	826.4	72.1	5.1	47.4	13.7

	C1			C2			C3		
	MIN	MAX	Ave	MIN	MAX	Ave	MIN	MAX	Ave
Turbidity (NTU)	0.0	1.9	0.2	0.0	10.3	0.7	0.9	28.9	10.3
DO (mg/l)	6.8	11.4	9.3	8.9	11.9	9.8	7.3	13.5	10.0
Suspended Solid (mg/l)	1.0	1.5	1.1	1.0	14.0	1.9	4.8	21.0	11.3

* Remarks: Detection limit for Turbidity, DO and SS are 1 NTU, 0.1 mg/L and 1 mg/L respectively.

5.6 Action and limit level for Water Quality

Based on the criteria stipulated in EM&A manual Section 4.8 and baseline water quality monitoring data obtained, the A/L levels are shown in Table 5.6.1 and Table 5.6.2. If the water quality monitoring results at any impact stations exceeded the criteria, the actions in accordance with the Event and Action Plan in Table 5.6.3 should be taken.

Table 5.6.1 Water quality criteria for monitoring

Parameters	Action	Limit
DO in mg/L (mid-depth)	- 5%-ile of baseline data	- 4mg/L
SS in mg/L (mid-depth)	- 95%-ile of baseline data; or - 120% of control station's SS on the same day of measurement	- 99%-ile of baseline; or - 130% of control station's SS on the same day of measurement
Turbidity in NTU (mid-depth)	- 95%-ile of baseline data; or - 120% of control station's turbidity on the same day of measurement	- 99%-ile of baseline; or - 130% of control station's turbidity on the same day of measurement

Table 5.6.2 Action and Limit Levels established according to baseline data

Parameters	Monitoring locations							
	M1		M2		M3		M4	
	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level
Turbidity (NTU)	15.2	16.9	5.3	6.5	16.8	26.0	16.2	18.0
DO (mg/L)	5.7	4.0	6.2	4.0	5.9	4.0	5.9	4.0
SS (mg/L)	12.2	12.8	3.1	4.2	12.4	17.7	13.9	15.2

Remarks:

For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits

For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table 5.6.3 Event and action Plan for Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level being exceed by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.
Action level being exceed by more than two consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; prepare to increase the monitoring frequency to daily 7. Repeat measurement on next day of exceedance 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER within three working days; 6. Implement the agreed mitigation measures.
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.

5.7 Water Quality Mitigation Measures

Construction Run-off and Drainage

The site practices outlined in ProPECC PN 1/94 ‘Construction Site Drainage’ should be followed as far as practicable during both construction and operation phase of the drainage improvement works in order to minimize surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge.

As recommended in the final EM&A manual, attention would be paid especially construction run-off and drainage, general construction activities, sewage discharged from construction workforce and river channel excavation works.

Contractor was recommended to provide sufficient water treatment facilities for accumulated site water and excavation activities carried out nearby river channel. Earth bunds should be provided to the construction site in / next to the river channel to form an enclosed, dry environment to minimize water quality impact.

For the generation of muddy water and accumulation of underground water in the sites, mitigation measures such as soak-away pond and temporary site water diversion channel were formed for site water treatment. Barriers formed by fine aggregates were also provided at the downstream area of the river channel acting as silt trap.

However, there are still gaps between the effectiveness of mitigation measures implemented by the Contractor and to comply with relevant requirements. Contractor was seriously recommended to review the condition of the site and implement necessary corrective actions and improvement works to avoid river contamination and flooding to the surrounding areas. ET will keep the practice on checking the effectiveness of mitigation measures, by site inspections, water quality monitoring and provision of recommendations, to minimize water quality impact from the project works.

5.8 Water Monitoring Schedule for the Next reporting period

Water monitoring scheduled for the next reporting period is 1, 7, 9, 12, 14, 16, 19, 20, 21, 26, 28 and 30 April 2010.

6. Ecology Monitoring

6.1 Ecological Monitoring Parameters

According to the Final EM&A Manual, a specific ecological monitoring programme of the improved section of PNH and LTT Rivers is recommended. The monitoring parameters required to measure in this project and survey methodology are described below:

- (1) Avifauna species and abundance: Birds will be surveyed quantitatively using transect count method. Birds within the river channel and on the riverbank will be identified and their abundance will be recorded.
- (2) Aquatic macroinvertebrate community species composition and abundance: Survey on aquatic fauna will focus on determination of the diversity and abundance of stream aquatic communities. Sampling methods, such as active searching, direct observation, netting, and kick sampling, will be determined according to the site conditions during field survey.
- (3) Fish community species composition and abundance: Sampling methods, such as active searching, direct observation, and hand netting, will be determined according to the site conditions during field survey.
- (4) Adult odonate community species composition and abundance: Adult dragonfly will be surveyed quantitatively using transect count method. Adult dragonflies within the river channel and on the riverbank will be identified and their abundance will be recorded. Species requiring close examination will be netted.
- (5) Aquatic, emergent and riparian vegetation community species composition and abundance: The area will be walked through. Plant species composition and their relative abundance will be recorded.
- (6) Surveys of White-shouldered Starling *Sturnus sinensis* will be conducted at the disused watchtowers next to LTT river. Breeding of the White-shouldered Starlings will be determined by checking signs of attempt to breed or sign of breeding which include carrying nesting materials, to-and-fro movement of adults carrying food, presence of recently fledged juveniles, etc. The number of breeding pairs and the site observation will be recorded whenever possible.

Water Quality Monitoring along LTT and PNH River as well as LTT bypass channel was carried out. Water quality monitoring will include Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Moreover, additional water monitoring parameters will be taken for the purposes of ecological monitoring of water quality in this project. The added information will include: BOD, Ammonia, Nitrate and Phosphate concentrations. Turbidity, DO, pH and water flow will be measured in-situ while water samples will be delivered to Accredited HOKLAS Laboratory accredited laboratory and the analyses followed the standard methods according to APHA Standard Methods for the Examination of Water and Wastewater, 20th Edition, or equivalent for analysis of SS, BOD, Ammonia, Nitrate and Phosphate concentrations.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site will be recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading will be discarded and further reading will be taken.

6.2 Monitoring Equipment and Methodology

Turbidity, DO, Salinity, pH and Temperature will be measured by a instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the

monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

6.3 Monitoring Locations

According to the Final EM&A Manual, the improved section of the river channels will be divided into 50m long sections, and ecological survey will be carried out in each of the 50m sections. A total of nine sections will be divided for the two rivers which include:

- Two sections for existing upstream of PNH river (i.e. the proposed 80m long trapezoidal channel)
- Two sections for existing downstream of PNH river (i.e. the proposed 100m long rectangular channel)
- Five sections for existing Luk Tei Tong River (i.e. the proposed 240m long trapezoidal channel)

The disused watchtowers are located at the confluence of the three rivers and next to LTT river.

The Location Plan for ecological is shown in Figure 6.1 for reference.

The improved sections of the river channels require to carrying out water quality monitoring for the ecological purpose. The sampling points for impact monitoring was undertaken in the same place as the baseline monitoring proposed, where include:

- Three points for existing of PNH river
- Three points for existing of Luk Tei Tong River

The Location Plan for ecological water monitoring is shown in Figure 6.2 for reference.

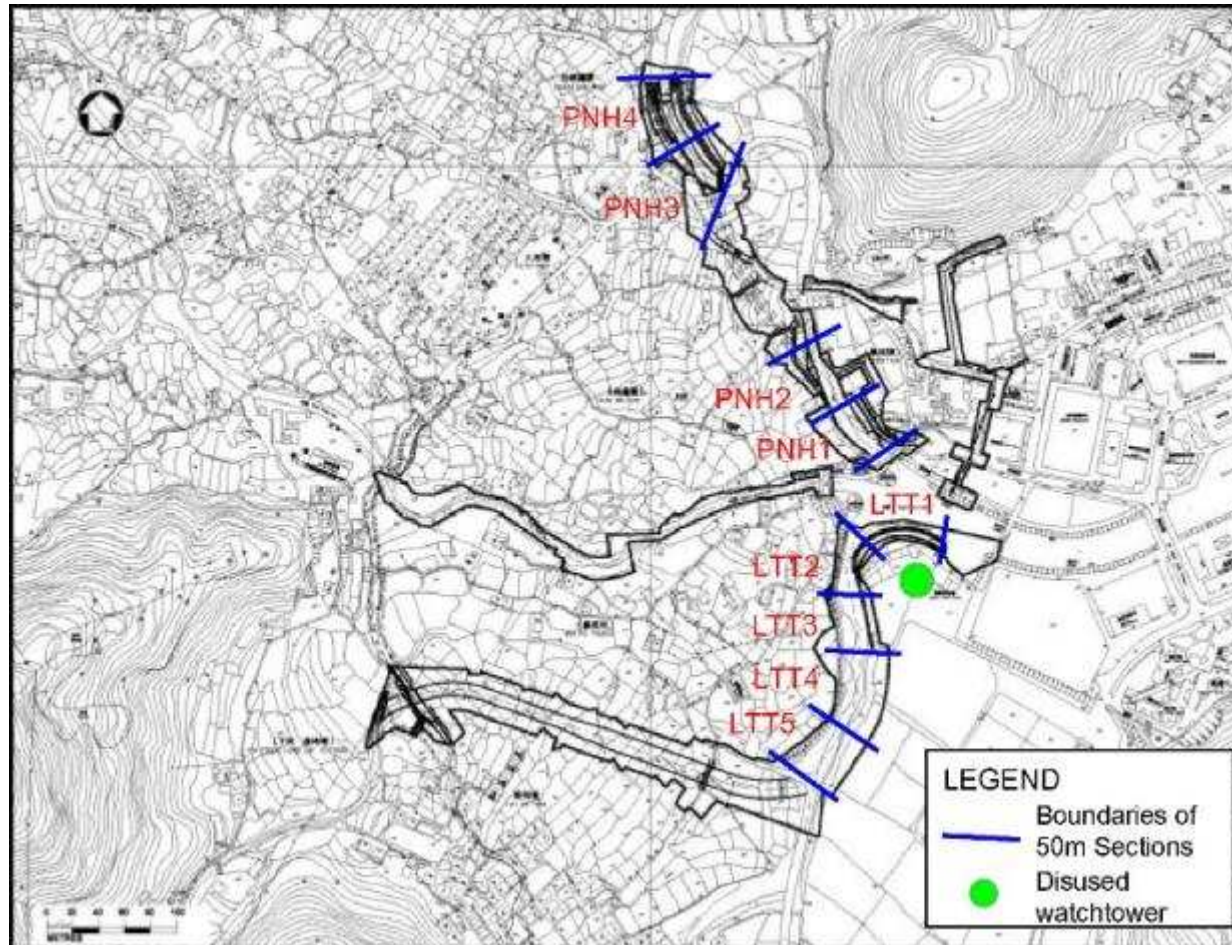


Figure 6.1 Ecological Monitoring Locations

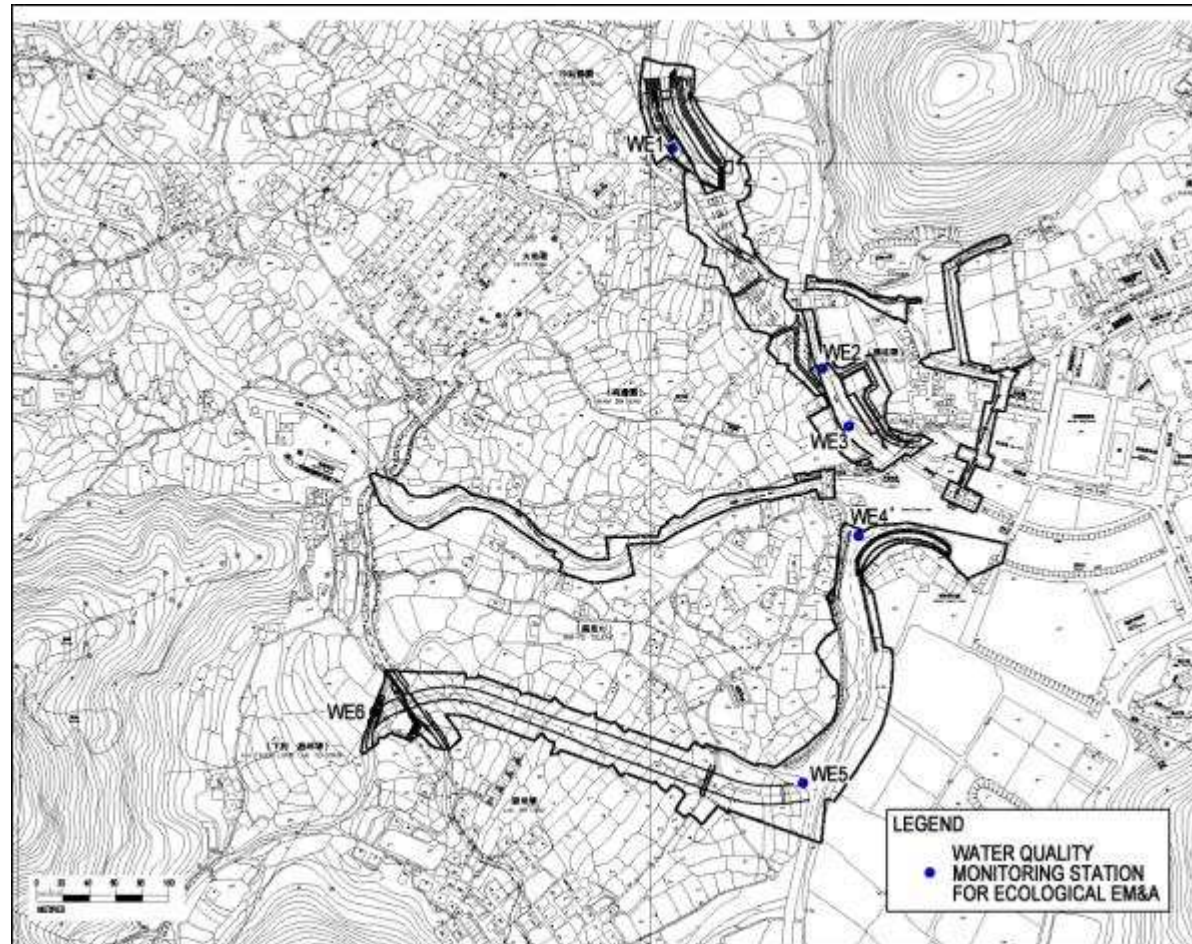


Figure 6.2 Ecological Water Quality monitoring locations

6.4 Monitoring Frequency

As proposed, ecological impact monitoring was carried out once for each monitoring location in the reporting month.

6.5 Monitoring results

Pak Ngan Heung Stream N and S sections

Vegetation

Surveys were conducted on 30 March 2010. During the current monitoring session, new rock gabion wall was under construction. Stream bank and stream bed of PNH3 was completely cleared. Stream bank of PNH4 was mostly cleared, while the weir is still intact.

The walk through survey recorded a total of 23 species, including 8 trees, 1 shrub, 7 herb and 4 grass species (Appendix D1) on PNH N section. 17 of the species recorded are natives, while 6 were exotics. Remnants of vegetation including native trees (e.g. *Ficus hispida*, *Macaranga tanarius*), aquatic floating plant (e.g. *Pistia stratioides*) and grasses species (e.g. *Microstegium ciliatum*) were still seen along the weir or retained at east stream bank. No species of conservation interest was recorded. No quantitative surveys were carried out on both PNH3 and PNH4 due to vegetation clearance and construction works on stream banks as part of the site clearance works under the project.

During the current monitoring session, construction work ongoing along PNH S section. Vegetation was only found on remnants of the old concrete bank. A total of 6 species recorded, 4 of which were native and 2 were exotic. It was composed of isolated individuals of mangrove (*Kandelia obovata*), exotic shrub (*Lantana camara*) and native trees (*Ficus supbera*, *Ficus microcarpa*) (Appendix D2). No species of conservation interest was recorded.

Terrestrial Fauna

Surveys were conducted on 5 March 2010.

One species of birds were recorded in the proposed work area of the Pak Ngan Heung River (Table 6.5.2). Common Koel *Eudynamis scolopacea* is common in Hong Kong.

Table 6.5.2 Avifauna in Pak Ngan Heung

Common names	Latin names	PNH 1	PNH 2	PNH 3	PNH 4	Commonness & distribution
Common Koel	<i>Eudynamis scolopacea</i>	1				CW

CW = common and widespread

No dragonfly was recorded in the proposed work area of the Pak Ngan Heung River in March 2010.

Aquatic fauna and fish

Sections of stream within the PNH3 boundary had been diverted to a bypass channel to facilitate the construction of the fish ladder. Therefore the PNH 3 was not covered by the present monitoring. In the remaining three survey section at PNH, 5 species of fish and 2 crustacean were recorded. All are common and widespread in Hong Kong. Fish species of conservation concern reported in the EIA report, i.e. Predaceous Chub and Flagtail *Kuhlia marginata*, was not recorded in PNH during the present monthly monitoring survey.

Table 6.5.4 Aquatic Invertebrates and fish in Pak Ngan Heung

Common names	Scientific names	PNH 1	PNH 2	PNH3	PNH4
Invertebrates					
Atyid shrimp	<i>Caridina elongata</i>			\	+
Palaemonid shrimp	<i>Macrobrachium hainanensis</i>			\	
Crab	<i>Varuna litterata</i>	+		\	+
Mitten Crab	<i>Eriocheir japonica</i>			\	
Fish					
Mosquito fish	<i>Gamusia affinis</i>			\	+
Goby	<i>Rhinogobius duospilus</i>			\	+
Barcheek Goby	<i>Rhinogobius giurinus</i>			\	
Swordtail	<i>Xiphophorus hellerii</i>			\	
Six-banded Barb	<i>Puntius semifasciolatus</i>			\	
Unidentified Cichlid fish				\	
Tilapia		+	++	\	
Predaceous Chub	<i>Parazacco spilurus</i>			\	
Jarboa Terapon	<i>Terapon jarbua</i>	++		\	
Common Silver-biddy	<i>Gerres oyena</i>			\	
Mullet	<i>Mugil cephalus</i>	+	+++	\	
Broken-band Hillstream Loach	<i>Liniparhomaloptera disparis</i>			\	

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Luk Tei Tong Stream Section

Vegetation

Surveys were conducted on 4 February 2010. During the current survey, site clearance was completed in most sections. Removal of old rock gabion at LLT1 was underway, while some remnants of grasses and mangroves remained at both LLT1 and LLT2 respectively.

The walk through survey recorded a total of 4 species, including 1 tree, and 3 grass species (Appendix D3). Two of the species recorded are natives, while 2 were exotics. No quantitative survey was carried out due to vegetation clearance on stream banks as part of the site clearance works under the project.

Terrestrial Fauna

The proposed work area of Luk Tei Tong River was divided into 5 sections. All recorded avifauna and dragonfly species are common in Hong Kong

Surveys were conducted on 5 March 2010.

A total of eight species of birds were recorded in these sections (Table 6.5.6). All these species are common and widely distributed in Hong Kong.

Table 6.5.6 Avifauna in Luk Tei Tong River

Common names	Latin names	LTT 1	LTT 2	LTT 3	LTT 4	LTT 5	Commonness & distribution
Little Egret	<i>Egretta garzetta</i>	1		1	1		CW
Great Egret	<i>Casmerodius albus</i>					1	CL
Grey Heron	<i>Ardea cinerea</i>	1					CL
Common Sandpiper	<i>Actitis hypoleucos</i>	1					CW
Common Koel	<i>Eudynamis scolopacea</i>	1					CW
White Wagtail	<i>Motacilla alba</i>	1					CW
Chinese Bulbul	<i>Pycnonotus sinensis</i>	1					CW
Magpie Robin	<i>Copsychus saularis</i>	1					CW

CW = common and widespread, CL = common/uncommon and localised

No dragonfly was recorded in the Luk Tei Tong River in January 2010.

Aquatic invertebrates and fish

4 species of fish, 2 species of crustacean and 2 species of mollusks were recorded in the 5 sections at LTT. All are common and widespread in Hong Kong. The two fish species of conservation concern reported in the EIA report, i.e. Flagtail *Kuhlia marginata* and Predaceous Chub *Parazacco spilurus* were not recorded in LTT during the present monitoring as well as the baseline monitoring survey.

Table 6.5.8 Aquatic invertebrates and fish in Luk Tei Tong River

Common names	Scientific names	LTT1	LTT2	LTT3	LTT4	LTT5
Invertebrates						
Mangrove clam	<i>Geloina erosa</i>					
Rock oyster	<i>Saccostrea cuculata</i>	++	++			
Snail	<i>Melanoides tuberculata</i>				+	+
Snail	<i>Terebralia</i> sp.					
Snail	<i>Nerita</i> sp.					
Snail	<i>Littoraria articulata</i>					
Crab	<i>Varuna litterata</i>	+				
Fiddler crab	<i>Uca lactea</i>					
Fiddler crab	<i>Uca arcuata</i>					
Fiddler crab	<i>Uca crassipes</i>					
Crab	<i>Perisesarma bidens</i>		+	+		
Mangrove mud crab	<i>Scylla paramamosain</i>					
Mitten crab	<i>Eriocheir japonica</i>					
Fish						
Common mudskipper	<i>Periophthalmus cantonensis</i>	+				
Tilapia		++	+	+		
Jarboa terapon	<i>Terapon jarbua</i>					
Mullet	<i>Mugil cephalus</i>	+++	++	++		
Common Silver-biddy	<i>Gerres oyena</i>					
Barcheek Goby	<i>Rhinogobius giurinus</i>				+	+

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Disused Watchtowers

Surveys were conducted on 5 March 2010.

There was no sign (e.g., adults carrying food or nesting materials) of use of the watchtower as nesting habitat by White-shouldered Starling.

White-shouldered Starling was not observed during the February 2010 monitoring. No bird of other species was observed entering the watchtower.

Since the monitoring surveys commenced in August 2008, no bird was observed entering the watchtower. It seems the birds do not prefer the watchtower as roosting or nesting habitat.

Ecological Water Quality Monitoring (EWQM)

EWQM was conducted on 1 March 2010. Monitoring results are summarized in Table 6.9. Detailed on-site measurements and laboratory report are presented in Appendix D4 and D5.

Table 6.10 shows the baseline results of Ecological Water Quality Monitoring, from the information given in Baseline Monitoring Report.

To review the results in Table 6.9 in general, the measured results of Suspended Solids and Turbidity measured in WE3 (PNH River) and WE4 (LTT River) was found higher than the previous months. Such facts were believed to be caused by disturbance of sediments, and site effluent discharge due to construction activities.

Table 6.9 Summarized Ecological water quality monitoring results (1 Mar 2010)

Parameters	Limit of detection	WE1	WE2	WE3	WE4	WE5	WE6
Suspended Solid (mg/l)	1	1.00	3.10	11.75	12.25	9.80	1.55
Nitrogen (Ammonia) (mg/l)	0.01	0.04	1.10	1.16	0.86	1.70	0.16
Nitrogen (Nitrate) (mg/l)	0.01	0.19	0.21	0.36	0.43	0.23	0.13
Phosphorous (mg/l)	0.01	0.05	0.13	0.12	0.12	0.39	0.04
BOD ₅ (mg/l)	1	1.00	5.00	4.00	1.00	3.00	1.00
DO (mg/l)	0.01	6.74	7.50	7.57	6.11	8.10	7.46
Turbidity (NTU)	0.1	0.00	4.25	13.85	9.35	4.50	0.00
Temperature (oC)	0.1	22.5	22.4	21.9	22.5	22.5	21.5
pH	0.01	7.11	7.61	7.61	7.01	7.22	6.78
Salinity (ppt)	0.1	0	0.4	2.9	12.5	4.2	0
Conductivity (ms/m)	0.1	15.8	100.0	532.0	2050.0	755.0	6.4
Water Flow (m/s)	N/A	0.01	0.02	0.02	0.01	0.02	0.01

Table 6.10 Baseline Results of Ecological water quality monitoring

Parameters	WE1	WE2	WE3	WE4	WE5	WE6
Suspended Solid (mg/l)	1.0	2.0	3.0	3.0	<1	<1
Nitrogen (Ammonia) (mg/l)	0.07	0.12	0.11	0.23	0.03	0.02
Nitrogen (Nitrate) (mg/l)	0.12	0.13	0.13	0.31	0.04	0.05
Phosphorous (mg/l)	0.04	0.06	0.06	0.09	0.06	0.05
BOD ₅ (mg/l)	<2	<2	<2	<2	<2	<2
DO (mg/l)	6.58	6.82	6.37	7.61	6.87	5.70
Turbidity (NTU)	4.44	5.12	5.93	6.96	4.65	2.73
PH	6.4	7.1	7.0	6.8	6.6	6.1
Salinity (ppt)	<0.1	0.1	0.3	7.6	0.1	<0.1

6.6 Action and Limit level for Monitoring of White-shouldered Starlings

A simple Event and Action Plan is shown in Table 6.6.1. Should the Event occur, action in accordance with the Action Plan should be carried out.

There was no recorded event in the reporting month.

Table 6.6.1 Event / Action Plan for Monitoring of White-shouldered Starlings

EVENT	ACTION	
	ET Leader	Contractor
Identification of disturbance to breeding White-shouldered Starlings	1. Increase frequency of monitoring to twice weekly	1. Check all construction actions and working methods
	2. Notify Site Engineer	2. Submit proposals for remedial action to prevent abandonment of the breeding site.
	3. Review construction activities of previous week.	3. Implement remedial action.
	4. Identify any changes in construction activities in previous week	4. Liaise with ET regarding effectiveness of remedial actions.
	5. Discuss remedial actions with Site Engineer	

6.7 Ecological monitoring Schedule

The next ecological surveys are scheduled on 9 and 13 April 2010, while ecological water quality monitoring is scheduled on 9 April 2010.

7. Action taken in Event of Exceedance

If the measurements (Noise, Water, Ecology) exceed the action / limit level, exceedance details will be reported and follow-up actions will be taken by relevant parties involved.

During the reporting period there was no exceedance for noise, ecological measurements recorded; therefore no actions were taken.

Total 80 non-compliance events of water quality limits (Turbidity and Suspended Solids) were recorded in this reporting month according to the established level. ET has arranged site investigations for the exceedance events. Except the reasons of natural fluctuation, 30 events were identified to be substantially attributable to improper site practices. As such, the contractor was strongly recommended to review their sites condition and working method. Necessary as well as effective mitigation measures have to be implemented to minimize water quality impact from project site activities.

The summary of non-compliance events for water quality exceedance is listed in Table 7.1 for reference.

Table 7.1 Summary of Non-compliance for Water Quality

Date	Location	Parameter	Level of exceedance	Main cause of exceedance
3/3/10	M3	Turbidity, S.S.	Limit Level	Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river
	M4	Turbidity, S.S.	Limit Level	
4/3/10	M3	Turbidity, S.S.	Limit Level	Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river
5/3/10	M1	Turbidity, S.S.	Limit Level	M1 – Muddy effluent was directly discharged from site BC15 / retaining wall C
	M3	Turbidity, S.S.	Limit Level	M3 & M4 – Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river
	M4	Turbidity, S.S.	Limit Level	
6/3/10	M1	Turbidity, S.S.	Limit Level	M1 – Muddy effluent was directly discharged from site BC15 / retaining wall C
	M3	Turbidity, S.S.	Limit Level	M3 & M4 – Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river
	M4	Turbidity, S.S.	Limit Level	
11/3/10	M3	Turbidity, S.S.	Limit Level	M3 – Water quality was affected by mal-practice observed on 6 Mar.
12/3/10	M3	Turbidity, S.S.	Limit Level	M3 – Water quality was affected by mal-practice observed on 6 Mar.
19/3/10	M1	Turbidity, S.S.	Limit Level	Soil runoff arisen from earth movement and excavation works for construction of retaining wall C
22/3/10	M1	Turbidity, S.S.	Limit Level	Soil runoff arisen from earth movement and excavation works for construction of retaining wall C
23/3/10	M1	Turbidity, S.S.	Limit Level	Soil runoff arisen from earth movement and excavation works for construction of retaining wall C
24/3/10	M1	Turbidity, S.S.	Limit Level	Soil runoff arisen from earth movement and excavation works for construction of retaining wall C

8. Construction waste disposal

It is the contractor's responsibility to ensure that all wastes produced during the construction phase for the drainage improvement works are handled, stored and disposed of in accordance with good waste management practices and EPD's regulation and requirement. Waste materials generated during construction activities, such as construction and demolition (C&D) material, chemical wastes and general refuse, are recommended to be audited at regular intervals to ensure that proper storage, transportation and disposal practices are being implemented.

Contractor has completed the registration of Waste Producer under the Waste Disposal (Chemical Waste)(General) Regulation. The Waste Producer Number, WPN 5213-950-Y2443-03 was assigned by EPD on 12 Aug 2008. The Contractor would be responsible for the implementation of any mitigation measure to minimize waste or redress problems arising from the waste materials.

Table 8.1 is a summary of figures of the construction wastes disposal provided by Contractor.

Table 8.1 Summary of Construction Waste Disposal

Month	Amount of Construction Waste disposed		
	Inert Waste (to Public Fill)	Non-inert Waste (to Landfill)	Chemical Waste (to treatment plant)
1 st to 31 st Mar 10	363.70 (ton)	10.50 (ton)	Nil
Total	24227.66 (ton)	171.93 (ton)	0

9. Status of Permits and Licenses obtained

Table 9.1 is the updated status of environmental related permits/ license obtained for the construction activities

Table 9 .1 Status of Permits and Licenses Obtained

Description	License / Permit No.#	Date of Issue	Date of Expiry	Remarks
Environmental Permit	EP-237/2005/A	05 Mar 2007	--	Issued
Varied Environmental Permit	EP-237/2005/B	23 April 2009	--	Issued
Registration of C&D Waste Producer	7006521	--	--	Issued
Chemical Waste Producer	5213-950-Y2443-03	12 Aug 2008	--	Issued
Construction Noise Permit	N/A	N/A	N/A	N/A
Effluent Discharge License	EP890/W2/XG032 EP890/W2/XG033 EP890/W2/XG034 EP890/W2/XG035 EP890/W2/XG036 EP890/W2/XG037 EP890/W2/XG038 EP890/W2/XG039 EP890/W2/XG040 EP890/W2/XG041	23 Oct 2008	31 Oct 2013	Issued

The contractor implemented various environmental mitigation measures as recommended in the Environmental Permit and Final Mitigation Measures Report. The implemented schedule is presented in Appendix H.

10. Complaint Log

There was no formal complaint received during the reporting month.

	Noise	Water	Ecology	Cultural	Others
March 2010	0	0	0	0	0
Total	0	1	0	0	0

11. Site Environmental Audits

Site Inspection

With an intention to ensure that appropriate environmental protection and pollution control mitigation measures are properly implemented, regular environmental site inspections have been scheduled.

Within the reporting month, site inspections were conducted on 4, 11, 18, 25 and 30 March 2010.

A detailed checklist of each site inspection together with comments, relevant photos and maps have been filed and kept. A summary of observation and follow-up action is shown in Table 11.1

Table 11.1 Summary of site inspection

Date	Observations	Advice from ET	Action taken	Closing Date
4, 11 & 18 Mar 10	Fuel drums and chemical containers were placed at the fish ladder site without secondary containment	Contractor was recommended to provide proper drip pans to the chemicals using on site; idling chemicals should be relocated to designate chemical storage area to minimize chemical spillage on site.	The concerned fuel and chemical containers were relocated to designate chemical storage area prior to the inspection on 25 Mar	25 Mar 10
26 Feb 10	Ashes from burning were left from PNH site retaining wall C during inspection.	Contractor was reminded open burning is prohibition. Also, ashes left at the site area should be collection and disposed as soon as possible.	The ashes was removed from site prior to the inspection on 4 Mar	4 Mar 10
26 Feb and 4 Mar 10	River water at the down stream area of LTT seawall observed to be turbid during inspection.	Contractor was advised to trace the cause of contamination. Should such condition was caused by project works Immediate corrective actions should be implemented to stop further deterioration of water quality.	Follow up action was taken as advised prior to the inspection on 11 Mar 10. No turbid water was observed during inspection	11 Mar 10
26 Feb and 4 Mar 10	No proper mitigation measures implemented to prevent soil run-off to the river channel from the haul access for mass concrete wall site.	Contractor was recommended to provide proper bund wall at the edge of the concerned haul access, exposed earthy bund wall should be well covered with geo-textile materials to prevent erosion.	Follow up action was taken as advised prior to the inspection on 18 Mar.	18 Mar 10
26 Feb & 25 Mar 10	Riverbanks of the diversion channel at PNH fish ladder, was directly exposed without protection	Contractor was advised to geo-textile coverings to the exposed diversion channel to prevent erosion therefore causing contamination to the river body	Prior to the inspection on 30 Mar, riverbanks without protection with vegetations were covered with geo-textile materials as recommended	Ongoing
26 Feb 10	Silt clay and muddy water accumulated in the wheel washing bay at site entrance of PNH fish ladder sit, was brought to the public access during inspection	Contractor was recommended to clean up the wheel washing bay once it was saturated with silt and muddy water as to avoid earth deposition to the public area	Follow up action was taken as advised prior to the inspection on 4 Mar.	4 Mar 10
4 Mar 10	No geo-textile covering provided to the earth bund of gabion wall site at LTTR	Contractor was advised to rectify such discrepancy as soon as possible to prevent erosion from causing	Follow up action was taken as advised prior to the inspection on 18 Mar	18 Mar 10

Table 11.1 Summary of site inspection

Date	Observations	Advice from ET	Action taken	Closing Date
		contamination		
11 & 30 Mar 10	Muddy water was accumulated in the wheel washing bay at the site entrance of PNH fish ladder site	Contractor was reminded to clean up the wheel washing bay to maintain its effectiveness regularly as part of site clean	To be followed in the next reporting period	Ongoing
18 Mar 10	Open stockpiles of earth materials were observed at the box culvert site of PNH	Contractor was recommended to provide tarpaulin coverings to the concerned stockpiles to prevent erosion and runoff	Follow up action was taken as advised prior to the inspection on 25 Mar	25 Mar 10
18 Mar 10	Pipelines diverting site water from LTT seawall site were observed to be damaged. Due to the site water leakage accumulation of stagnant water on the site ground was also found	Contractor was advised to implement follow up action to stop further leakage. Stagnant water should be drained to prevent mosquito breeding	Follow up action was taken as advised prior to the inspection on 25 Mar	25 Mar 10
25 & 30 Mar 10	Open stockpiles of earth materials were observed at LTT site box culvert A	Contractor was recommended to provide tarpaulin coverings to the concerned stockpiles to prevent erosion and runoff	To be followed in the next reporting period	Ongoing
25 Mar 10	No protective measure implemented to avoid surface runoff entering into the river channel from the haul access at LTT seawall site as well as retaining wall site PNH	Contractor was recommended to provide proper bund walls and barriers along edges of the concerned haul access as soon as possible	To be followed in the next reporting period	Ongoing
30 Mar 10	Geo-textile coverings for the part of riverbanks were found removed during inspection	Contractor was requested to rectify such discrepancy immediately to prevent erosion and site water runoff.	To be followed in the next reporting period	Ongoing
30 Mar 10	Site water diversion pipeline at PNH seawall site was found damaged. Site water being leaked out caused erosion to the edge of the haul access where is connected with the	Contractor was advised to replace the damages hose and implement rectification to the eroded haul access as soon as possible	To be followed in the next reporting period	Ongoing

Table 11.1 Summary of site inspection

Date	Observations	Advice from ET	Action taken	Closing Date
	pond of Yuen's Compound			
30 Mar 10	Chemicals for the construction of retaining wall C at PNH was found placed on the edge of the haul access during inspection	To prevent potential chemical spillage to the surrounding environment and river course, Contractor was recommended to assign a proper area with proper spillage containment measures implemented for chemicals using on the concerned site area.	To be followed in the next reporting period	Ongoing

11.2 Compliance with legal and Contractual requirement

ET leader has reviewed the progress and programme of the works to check any relevant environmental laws has not violated.

A non-compliance event regarding consecutive direct discharge of muddy effluent was recorded during routine water quality monitoring conducted on 3, 4, 5 and 6 March 2010 at monitoring stations M3 (Luk Tei Tong River) and M4 (Silver River).

In regard to the condition of water quality, an investigation was made by inspector from Environmental Protection Department on 9 March 2010 and a yellow form was issued to the Contractor.

Contractor was seriously recommended to implement necessary as well as effective mitigation measures to minimize water quality impact arisen from construction activities to the river streams. Any site water, underground water and waste water arising from construction should be diverted to proper site water treatment facilities before discharge.

Contractor took the advice and implement follow up action prior to the inspection on 11 March 2010. Site water generated from construction of river wall was diverted to a de-silting tank and then to a soak-away pond for de-silting. Direct discharge of site water was not observed during the follow up inspection.

11.3 Environmental Complaint and follow up actions

During this reporting period, there was no documented complaint received. Therefore, follow up actions for the environmental complaint is not required.

12. Future key issues

As informed by contractor major site activities in the upcoming will include construction of box culverts, retaining walls, gabion walls, sloping sea wall and fish ladder on project sites. It is expected that several impacts on environmental aspects will be generated on-site. With reference to the EM&A manual, mitigation measure report as well as the environmental permit, proper mitigation measures are proposed to be taken, if necessary.

Contractor was reminded again to provide proper measures to mitigate water quality impacts to the river channels due to construction works. River based construction sites should be well enclosed by bunds in dry condition, as to prevent surface run-off and site water seepage to the stream. Bare soil surface, which is directly exposed to the river channel in the site area, should be completely covered with geo-textile to prevent soil erosion. For river-based and any construction activities carried at riverside, contractor should implement proper protection measures such as barriers and/or silt curtains to prevent surface run-off from entering water bodies.

Underground water and site water may be accumulated on site. Contractor is recommended to treat the accumulated site water by proper silt removal facilities before discharging to the designated discharge point; reuse of site water should be considered also. Channel, trench and manholes connected with project sites should be sealed to prevent site water and any construction materials entering public drainage and causing water quality impact.

Construction activities such as backfilling, earth movement may generate dust impact to the vicinity of sensitive receivers. Contractor is advised to provide regular water spraying for the dusty static area. Stockpiling may be found on site and those should be covered by tarpaulin to prevent erosion and run-off.

Heavy plants and vehicles may be deployed for the construction and those would generate certain noise impacts to the sensitive receivers. Noisy activities should be well planned and scheduled to avoid parallel operation of multiple plants, so as to minimize noise impacts to the nearby sensitive receivers.

Construction activities and operation of site equipments may require use of chemicals and fuel on site. Secondary containment and spillage preventative measures should be implemented to such chemicals using on site.

13. Conclusions

In this reporting month, major site activities included haul access formation, construction of retaining walls, gabion wall and box culvert at PNH River and LTT River respectively.

Regular site meetings and inspection audits led by the seniors for discussing site environmental matters were held among Project Proponent, Contractor and the ET on weekly basis. Also monthly site meeting and inspection audits with the above parties and IEC were carried out on 25 March 2010.

For noise level monitoring, all results were within the established A/L limits.

For water quality monitoring, total 80 non-compliance events of water quality criteria were recorded in this reporting month. Except the natural fluctuation, 30 events were believed to be caused by improper site practices. Hence, the contractor was urged to review the site condition and implement necessary mitigation measures and corrective actions as soon as possible to minimize water quality impact due to site works.

During ecological monitoring survey, no White-shouldered Starling was recorded breeding in the watch tower. Some drainage improvement works were on-going at a distance from the watchtower on inter-tidal areas at downstream of Luk Tei Tong River (LTT1). The works area was screened from the watchtower by tall plantations. The absence of nesting of White-shouldered Starling in the watch tower did not seem to be related to construction works in Luk Tei Tong River. A bird species nests in village houses should be to certain extent disturbance tolerant.

No bird was observed entering the watchtower since the monitoring surveys commenced in August 2008. Also, no breeding was recorded in the baseline survey in September 2007. It appears that the birds do not prefer to roost or nest in the watch tower.

In regard to the muddy effluent discharge causing contamination to the river channel, site investigation was made by inspector from Environmental Protection Department and a yellow form was issued to the Contractor. As such, Contractor was seriously recommended to implement necessary environmental mitigation measures to address the environmental concerns.

Site water control was the major concern in this reporting month. Therefore, ET recommended the contractor to implement sufficient and effective mitigation measures to minimize water quality impact from site works. Proper de-silting facilities should be provided for site water treatment. To prevent surface run-off and soil erosion from site activities, earth bunds with complete coverage of geo-textile materials should be formed at river-based and/or riverside project sites. Contractor should be cautious on change of river water quality, immediate corrective action was required once muddy effluent discharge, or disturbance of sediment was found from site works.

ET has reminded the contractor to provide environmental pollution control measures wherever necessary; and to keep a good environmental management at site practice.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement.

Appendix A

Construction

Programmer and







Location plan

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	%	Predecessors	2008												2009												2010												2011											
								JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB										
7010	Preparation for works (Minor Portion)	131	0	18JAN2008 A	27MAY2008 A	100	0001	Preparation for works (Minor Portion)																																															
7020	Non-working Period at TWT Beach (1)	196	0	01APR2008 A	13OCT2008 A	100		Non-working Period at TWT Beach (1)																																															
7030	uPVC Sewer (DN160-400) M/H A16 - M/H A34	465	30	28MAY2008 A	04SEP2009	94	7010	uPVC Sewer (DN160-400) M/H A16 - M/H A34																																															
7040	uPVC Sewer (DN160-400) M/H A15 - M/H A13	50	0	14OCT2008 A	02DEC2008 A	100	7020	uPVC Sewer (DN160-400) M/H A15 - M/H A13																																															
7050	uPVC Sewer (DN160-400) M/H A11 - M/H A7	50	0	03DEC2008 A	21JAN2009 A	100	7040	uPVC Sewer (DN160-400) M/H A11 - M/H A7																																															
7060	uPVC Sewer (DN160-400) M/H A1 - M/H A3	65	0	22JAN2009 A	27MAR2009 A	100	7050	uPVC Sewer (DN160-400) M/H A1 - M/H A3																																															
8000	Sewerage works at PNH (S4)	772	206	18JAN2008 A	27FEB2010	73	0001	Sewerage works at PNH (S4)																																															
8010	Preparation of works	168	0	07JAN2008 A	22JUN2008 A	100		Preparation of works																																															
8020	uPVC Sewer (DN160-400) M/H ED2 -D28 - D118	320	0	23JUN2008 A	08MAY2009 A	100	8010	uPVC Sewer (DN160-400) M/H ED2 -D28 - D118																																															
8030	uPVC Sewer (DN160-400) M/H D1 - D27	280	191	09MAY2009 A	12FEB2010	32	8020	uPVC Sewer (DN160-400) M/H D1 - D27																																															
9000	Preservation & Protection of Exist Trees	534 *	534 *	06AUG2009	21JAN2011	0	0001	Preservation & Protection of Exist Trees																																															
9010	Preparton for works	100	0	07JAN2008 A	15APR2008 A	100		Preparton for works																																															
9020	Protection & Transplanting Works	1011	534	16APR2008 A	21JAN2011	47	9010	Protection & Transplanting Works																																															

Start date 07JAN2008
 Finish date 21JAN2011
 Data date 06AUG2009
 Run date 15AUG2009
 Page number 6A
 Primavera Systems, Inc.

Yick Hing Construction Co. Ltd.

Drainage Improvement Work in South Lantau
 and Construction of Mui Wo Village Sewerage Phase 1
 Master Programme (Rev.9b)

-  Early bar
-  Progress bar
-  Critical bar
-  Summary bar
-  Start milestone point
-  Finish milestone point

NOTES :

1. ALL LEVELS ARE IN METRES ABOVE P.D.H.K.1.
2. ALL GRIDS REFER TO HONG KONG 1980 GRID.

LEGENDS :

- SITE BOUNDARIES
- PORTION D1 - PAK NGAM BEIANG
- PORTION D2 - LING TSUI TAI LAI
- PORTION D3 - LING TSUI TAI (B)
- PORTION D4 - TAI TEI TONG RIVER
- PORTION D5 - LUK TEI TONG
- PORTION D6 - FUU O
- PORTION D7 - LO UK TSEEN
- PORTION D8 - CHEUNG SHA SHEUNG YEGHEN
- PORTION D9 - EMERGENCY VEHICULAR ACCESS (EVA) AT BUI 'N'

FOR TENDER PURPOSES ONLY

DRAWING NO. DC/2006/11		DATE 12 FEB 2006	
FILE NO. DP/06/4128CD		DATE 23 MAR 2006	
PROJECT NO. 128CD		DATE 10 MAY 2007	
CONTRACT		DATE 11 MAY 2007	
DESIGNED BY H. Y. CHAN 12 FEB 2006			
DRAWN BY B. D. CHAN 23 MAR 2006			
CHECKED BY W. H. CHAN 10 MAY 2007			
VERTICAL BY T. Y. CHAN 11 MAY 2007			
APPROVED			

DESIGNED BY H. Y. CHAN 12 FEB 2006
 DRAWN BY B. D. CHAN 23 MAR 2006
 CHECKED BY W. H. CHAN 10 MAY 2007
 VERTICAL BY T. Y. CHAN 11 MAY 2007
 APPROVED

CONTRACT NO. DC/2006/11
 FILE NO. DP/06/4128CD
 PROJECT NO. 128CD
 CONTRACT

DRAINAGE IMPROVEMENT IN SOUTHERN LANTAU


PORTIONS OF SITE - SOUTHERN LANTAU

drawing title
 sheet 1 of 2
 drawing no.
 scale
 DDN/128CDZ/1002A 1 : 2000

OFFICE COPYRIGHT RESERVED

DRAINAGE PROJECTS DIVISION

DRAINAGE SERVICES DEPARTMENT
 GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION

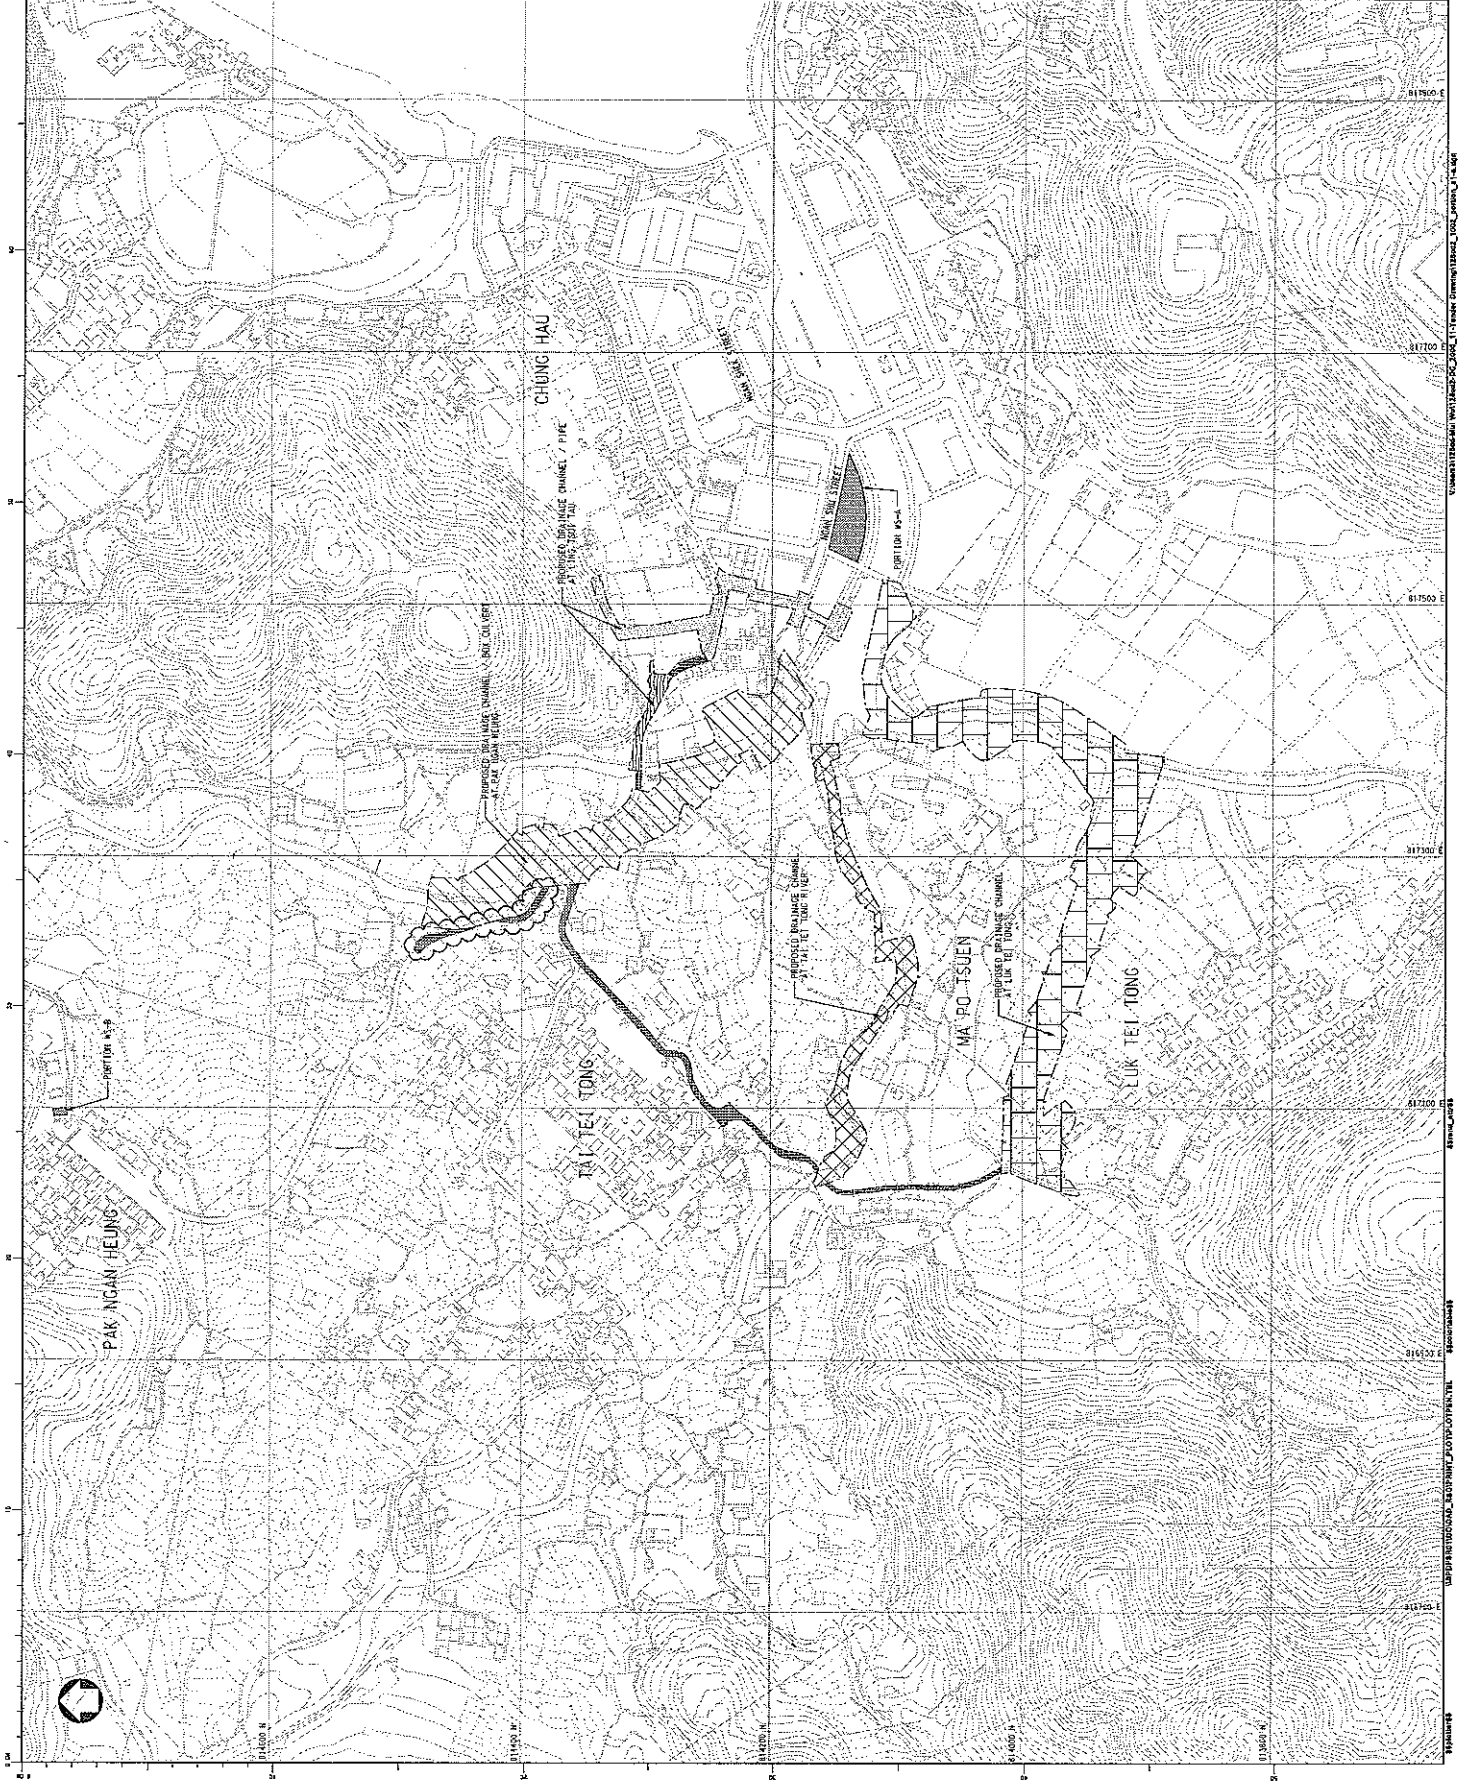

81700 E
 81750 E
 81800 E
 81850 E
 81900 E
 81950 E
 82000 E
 82050 E
 82100 E
 82150 E
 82200 E
 82250 E
 82300 E
 82350 E
 82400 E
 82450 E
 82500 E
 82550 E
 82600 E
 82650 E
 82700 E
 82750 E
 82800 E
 82850 E
 82900 E
 82950 E
 83000 E
 83050 E
 83100 E
 83150 E
 83200 E
 83250 E
 83300 E
 83350 E
 83400 E
 83450 E
 83500 E
 83550 E
 83600 E
 83650 E
 83700 E
 83750 E
 83800 E
 83850 E
 83900 E
 83950 E
 84000 E
 84050 E
 84100 E
 84150 E
 84200 E
 84250 E
 84300 E
 84350 E
 84400 E
 84450 E
 84500 E
 84550 E
 84600 E
 84650 E
 84700 E
 84750 E
 84800 E
 84850 E
 84900 E
 84950 E
 85000 E
 85050 E
 85100 E
 85150 E
 85200 E
 85250 E
 85300 E
 85350 E
 85400 E
 85450 E
 85500 E
 85550 E
 85600 E
 85650 E
 85700 E
 85750 E
 85800 E
 85850 E
 85900 E
 85950 E
 86000 E
 86050 E
 86100 E
 86150 E
 86200 E
 86250 E
 86300 E
 86350 E
 86400 E
 86450 E
 86500 E
 86550 E
 86600 E
 86650 E
 86700 E
 86750 E
 86800 E
 86850 E
 86900 E
 86950 E
 87000 E
 87050 E
 87100 E
 87150 E
 87200 E
 87250 E
 87300 E
 87350 E
 87400 E
 87450 E
 87500 E
 87550 E
 87600 E
 87650 E
 87700 E
 87750 E
 87800 E
 87850 E
 87900 E
 87950 E
 88000 E
 88050 E
 88100 E
 88150 E
 88200 E
 88250 E
 88300 E
 88350 E
 88400 E
 88450 E
 88500 E
 88550 E
 88600 E
 88650 E
 88700 E
 88750 E
 88800 E
 88850 E
 88900 E
 88950 E
 89000 E
 89050 E
 89100 E
 89150 E
 89200 E
 89250 E
 89300 E
 89350 E
 89400 E
 89450 E
 89500 E
 89550 E
 89600 E
 89650 E
 89700 E
 89750 E
 89800 E
 89850 E
 89900 E
 89950 E
 90000 E
 90050 E
 90100 E
 90150 E
 90200 E
 90250 E
 90300 E
 90350 E
 90400 E
 90450 E
 90500 E
 90550 E
 90600 E
 90650 E
 90700 E
 90750 E
 90800 E
 90850 E
 90900 E
 90950 E
 91000 E
 91050 E
 91100 E
 91150 E
 91200 E
 91250 E
 91300 E
 91350 E
 91400 E
 91450 E
 91500 E
 91550 E
 91600 E
 91650 E
 91700 E
 91750 E
 91800 E
 91850 E
 91900 E
 91950 E
 92000 E
 92050 E
 92100 E
 92150 E
 92200 E
 92250 E
 92300 E
 92350 E
 92400 E
 92450 E
 92500 E
 92550 E
 92600 E
 92650 E
 92700 E
 92750 E
 92800 E
 92850 E
 92900 E
 92950 E
 93000 E
 93050 E
 93100 E
 93150 E
 93200 E
 93250 E
 93300 E
 93350 E
 93400 E
 93450 E
 93500 E
 93550 E
 93600 E
 93650 E
 93700 E
 93750 E
 93800 E
 93850 E
 93900 E
 93950 E
 94000 E
 94050 E
 94100 E
 94150 E
 94200 E
 94250 E
 94300 E
 94350 E
 94400 E
 94450 E
 94500 E
 94550 E
 94600 E
 94650 E
 94700 E
 94750 E
 94800 E
 94850 E
 94900 E
 94950 E
 95000 E
 95050 E
 95100 E
 95150 E
 95200 E
 95250 E
 95300 E
 95350 E
 95400 E
 95450 E
 95500 E
 95550 E
 95600 E
 95650 E
 95700 E
 95750 E
 95800 E
 95850 E
 95900 E
 95950 E
 96000 E
 96050 E
 96100 E
 96150 E
 96200 E
 96250 E
 96300 E
 96350 E
 96400 E
 96450 E
 96500 E
 96550 E
 96600 E
 96650 E
 96700 E
 96750 E
 96800 E
 96850 E
 96900 E
 96950 E
 97000 E
 97050 E
 97100 E
 97150 E
 97200 E
 97250 E
 97300 E
 97350 E
 97400 E
 97450 E
 97500 E
 97550 E
 97600 E
 97650 E
 97700 E
 97750 E
 97800 E
 97850 E
 97900 E
 97950 E
 98000 E
 98050 E
 98100 E
 98150 E
 98200 E
 98250 E
 98300 E
 98350 E
 98400 E
 98450 E
 98500 E
 98550 E
 98600 E
 98650 E
 98700 E
 98750 E
 98800 E
 98850 E
 98900 E
 98950 E
 99000 E
 99050 E
 99100 E
 99150 E
 99200 E
 99250 E
 99300 E
 99350 E
 99400 E
 99450 E
 99500 E
 99550 E
 99600 E
 99650 E
 99700 E
 99750 E
 99800 E
 99850 E
 99900 E
 99950 E
 100000 E
 100050 E
 100100 E
 100150 E
 100200 E
 100250 E
 100300 E
 100350 E
 100400 E
 100450 E
 100500 E
 100550 E
 100600 E
 100650 E
 100700 E
 100750 E
 100800 E
 100850 E
 100900 E
 100950 E
 101000 E
 101050 E
 101100 E
 101150 E
 101200 E
 101250 E
 101300 E
 101350 E
 101400 E
 101450 E
 101500 E
 101550 E
 101600 E
 101650 E
 101700 E
 101750 E
 101800 E
 101850 E
 101900 E
 101950 E
 102000 E
 102050 E
 102100 E
 102150 E
 102200 E
 102250 E
 102300 E
 102350 E
 102400 E
 102450 E
 102500 E
 102550 E
 102600 E
 102650 E
 102700 E
 102750 E
 102800 E
 102850 E
 102900 E
 102950 E
 103000 E
 103050 E
 103100 E
 103150 E
 103200 E
 103250 E
 103300 E
 103350 E
 103400 E
 103450 E
 103500 E
 103550 E
 103600 E
 103650 E
 103700 E
 103750 E
 103800 E
 103850 E
 103900 E
 103950 E
 104000 E
 104050 E
 104100 E
 104150 E
 104200 E
 104250 E
 104300 E
 104350 E
 104400 E
 104450 E
 104500 E
 104550 E
 104600 E
 104650 E
 104700 E
 104750 E
 104800 E
 104850 E
 104900 E
 104950 E
 105000 E
 105050 E
 105100 E
 105150 E
 105200 E
 105250 E
 105300 E
 105350 E
 105400 E
 105450 E
 105500 E
 105550 E
 105600 E
 105650 E
 105700 E
 105750 E
 105800 E
 105850 E
 105900 E
 105950 E
 106000 E
 106050 E
 106100 E
 106150 E
 106200 E
 106250 E
 106300 E
 106350 E
 106400 E
 106450 E
 106500 E
 106550 E
 106600 E
 106650 E
 106700 E
 106750 E
 106800 E
 106850 E
 106900 E
 106950 E
 107000 E
 107050 E
 107100 E
 107150 E
 107200 E
 107250 E
 107300 E
 107350 E
 107400 E
 107450 E
 107500 E
 107550 E
 107600 E
 107650 E
 107700 E
 107750 E
 107800 E
 107850 E
 107900 E
 107950 E
 108000 E
 108050 E
 108100 E
 108150 E
 108200 E
 108250 E
 108300 E
 108350 E
 108400 E
 108450 E
 108500 E
 108550 E
 108600 E
 108650 E
 108700 E
 108750 E
 108800 E
 108850 E
 108900 E
 108950 E
 109000 E
 109050 E
 109100 E
 109150 E
 109200 E
 109250 E
 109300 E
 109350 E
 109400 E
 109450 E
 109500 E
 109550 E
 109600 E
 109650 E
 109700 E
 109750 E
 109800 E
 109850 E
 109900 E
 109950 E
 110000 E
 110050 E
 110100 E
 110150 E
 110200 E
 110250 E
 110300 E
 110350 E
 110400 E
 110450 E
 110500 E
 110550 E
 110600 E
 110650 E
 110700 E
 110750 E
 110800 E
 110850 E
 110900 E
 110950 E
 111000 E
 111050 E
 111100 E
 111150 E
 111200 E
 111250 E
 111300 E
 111350 E
 111400 E
 111450 E
 111500 E
 111550 E
 111600 E
 111650 E
 111700 E
 111750 E
 111800 E
 111850 E
 111900 E
 111950 E
 112000 E
 112050 E
 112100 E
 112150 E
 112200 E
 112250 E
 112300 E
 112350 E
 112400 E
 112450 E
 112500 E
 112550 E
 112600 E
 112650 E
 112700 E
 112750 E
 112800 E
 112850 E
 112900 E
 112950 E
 113000 E
 113050 E
 113100 E
 113150 E
 113200 E
 113250 E
 113300 E
 113350 E
 113400 E
 113450 E
 113500 E
 113550 E
 113600 E
 113650 E
 113700 E
 113750 E
 113800 E
 113850 E
 113900 E
 113950 E
 114000 E
 114050 E
 114100 E
 114150 E
 114200 E
 114250 E
 114300 E
 114350 E
 114400 E
 114450 E
 114500 E
 114550 E
 114600 E
 114650 E
 114700 E
 114750 E
 114800 E
 114850 E
 114900 E
 114950 E
 115000 E
 115050 E
 115100 E
 115150 E
 115200 E
 115250 E
 115300 E
 115350 E
 115400 E
 115450 E
 115500 E
 115550 E
 115600 E
 115650 E
 115700 E
 115750 E
 115800 E
 115850 E
 115900 E
 115950 E
 116000 E
 116050 E
 116100 E
 116150 E
 116200 E
 116250 E
 116300 E
 116350 E
 116400 E
 116450 E
 116500 E
 116550 E
 116600 E
 116650 E
 116700 E
 116750 E
 116800 E
 116850 E
 116900 E
 116950 E
 117000 E
 117050 E
 117100 E
 117150 E
 117200 E
 117250 E
 117300 E
 117350 E
 117400 E
 117450 E
 117500 E
 117550 E
 117600 E
 117650 E
 117700 E
 117750 E
 117800 E
 117850 E
 117900 E
 117950 E
 118000 E
 118050 E
 118100 E
 118150 E
 118200 E
 118250 E
 118300 E
 118350 E
 118400 E
 118450 E
 118500 E
 118550 E
 118600 E
 118650 E
 118700 E
 118750 E
 118800 E
 118850 E
 118900 E
 118950 E
 119000 E
 119050 E
 119100 E
 119150 E
 119200 E
 119250 E
 119300 E
 119350 E
 119400 E
 119450 E
 119500 E
 119550 E
 119600 E
 119650 E
 119700 E
 119750 E
 119800 E
 119850 E
 119900 E
 119950 E
 120000 E
 120050 E
 120100 E
 120150 E
 120200 E
 120250 E
 120300 E
 120350 E
 120400 E
 120450 E
 120500 E
 120550 E
 120600 E
 120650 E
 120700 E
 120750 E
 120800 E
 120850 E
 120900 E
 120950 E
 121000 E
 121050 E
 121100 E
 121150 E
 121200 E
 121250 E
 121300 E
 121350 E
 121400 E
 121450 E
 121500 E
 121550 E
 121600 E
 121650 E
 121700 E
 121750 E
 121800 E
 121850 E
 121900 E
 121950 E
 122000 E
 122050 E
 122100 E
 122150 E
 122200 E
 122250 E
 122300 E
 122350 E
 122400 E
 122450 E
 122500 E
 122550 E
 122600 E
 122650 E
 122700 E
 122750 E
 122800 E
 122850 E
 122900 E
 122950 E
 123000 E
 123050 E
 123100 E
 123150 E
 123200 E
 123250 E
 123300 E
 123350 E
 123400 E
 123450 E
 123500 E
 123550 E
 123600 E
 123650 E
 123700 E
 123750 E
 123800 E
 123850 E
 123900 E
 123950 E
 124000 E
 124050 E
 124100 E
 124150 E
 124200 E
 124250 E
 124300 E
 124350 E
 124400 E
 124450 E
 124500 E
 124550 E
 124600 E
 124650 E
 124700 E
 124750 E
 124800 E
 124850 E
 124900 E
 124950 E
 125000 E
 125050 E
 125100 E
 125150 E
 125200 E
 125250 E
 125300 E
 125350 E
 125400 E
 125450 E
 125500 E
 125550 E
 125600 E
 125650 E
 125700 E
 125750 E
 125800 E
 125850 E
 125900 E
 125950 E
 126000 E
 126050 E
 126100 E
 126150 E
 126200 E
 126250 E
 126300 E
 126350 E
 126400 E
 126450 E
 126500 E
 126550 E
 126600 E
 126650 E
 126700 E
 126750 E
 126800 E
 126850 E
 126900 E
 126950 E
 127000 E
 127050 E
 127100 E
 127150 E
 127200 E
 127250 E
 127300 E
 127350 E
 127400 E
 127450 E
 127500 E
 127550 E
 127600 E
 127650 E
 127700 E
 127750 E
 127800 E
 127850 E
 127900

Appendix B Key Personal Contact information chart

Organization Name	Role	Title	Name	Telephone	Fax Number
Drainage Service Department	Project Proponent	Engineering Representative	Mr. Chan Wai Hong	2594 7464	2827 8700
Ellied Environmental Consultants Limited	Independent Environmental Checker (IEC)	Principal Consultant	Ms. Grace Kwok	2815 7028	2815 5399
Yick-Hing Construction Company Limited	Main Contractor	Senior Project Manager	Mr. Liu Kai Choi	2394 4988	2787 4890
Environmental Pioneers & Solutions Limited	Environmental Team (ET)	Environmental Team Leader	Ms. Patricia Chung	2965 0888	2856 2010



华南国家计量测试中心
广东省计量科学研究院
SOUTH CHINA NATIONAL CENTER OF METROLOGY
GUANGDONG INSTITUTE OF METROLOGY



检定证书

VERIFICATION CERTIFICATE

证书编号: SSD20093126
Certificate No.

第 1 页 共 3 页
Page of

委托方
Client

委托方地址
Add. of Client

计量器具名称: Sound Level Calibrator
Description

型号规格: 4231
Model/Type

制造厂: B & K
Manufacturer

出厂编号: 1820929/E-028-4
Serial No.

接收日期: 2009年 9月 21日
Date of Receipt Y M D

结论: 1级合格 (Class 1)
Conclusion

检定日期: 2009年 9月 22日
Date of Verification Y M D

依据检定规程, 被检仪器检定周期为 壹 年
The verification period is 1 Year(s)

批准人: [Signature]
Approved Signatory

核 验: [Signature]
Inspected by

检 定: [Signature]
Verified by

证书专用章

本中心地址: 中国广州市广园中路松柏东街30号 邮政编码: 510405
电话: (8620)86594172 传真: (8620)86590743 E-mail: scm@scm.com.cn
Add: No.30, Songbaidong Street, Guangyuanzhong Road, Guangzhou, P. R. China
Post Code: 510405 Tel: (8620)86594172 Fax: (8620)86590743

090921P01 2



华南国家计量测试中心
广东省计量科学研究院
SOUTH CHINA NATIONAL CENTER OF METROLOGY
GUANGDONG INSTITUTE OF METROLOGY



说 明

证书编号: SSD20093126
Certificate No.:

DIRECTIONS

第 2 页 共 3 页
Page of

1. 本中心是国家质量监督检验检疫总局在华南地区设立的国家法定计量检定机构, 计量授权证书号是(国)法计(2007)01043号, (国)法计(2007)01032号。
This laboratory is the National Legal Metrological Verification Institution in southern China set up by the General Administration of Quality Supervision, Inspection and Quarantine of the People's Republic of China (AQSIQ) under authorization certificates No. (2007)01043 & (2007)01032.
2. 本中心所出具的数据均可溯源至保存在中国计量科学研究院的国家计量基准和国际单位制(SI); 中国计量科学研究院于1999年代表中国签署了“国家计量基准及国家计量研究院出具的校准和测量证书相互承认协议”。
All data issued by this laboratory are traceable to national primary standards maintained in National Institute of Metrology (NIM) and International System of Units (SI). NIM is the signatory to the Mutual Recognition Arrangement (MRA) for national measurement standards and for calibration and measurement certificates issued by national metrology institutes.
3. 本次检定的技术依据
Reference documents for the verification:
JJG 176-2005 声校准器检定规程 V.R. of Sound Calibrators.

4. 本次检定所使用的主要计量标准器具
Major standards of measurement used in the verification:

设备名称/型号 Name of Equipment (Model)	编号 Serial No.	证书号/有效期 Certificate No. (Due Date)	计量特性 Metrological Characteristic
电声标准装置 Sound Level Meters Verification Device	声01	[1992] 国量标检定字 第085号 /2010-01-08	声压级: (0.4~110) dB(k=2) 在参考频率上: 0.08 dB(k=2) (压力场) Sound Level Meters: 0.3 dB(k=2); Sound Calibrator 0.15 dB(k=2)

5. 检定地点、环境条件

Place and environmental conditions of the verification:

地点: 声学/振动实验室 温度: (23±3) °C 相对湿度: (40~80) %
Place: Acoustics/Vibration Lab. Temperature RH

6. 被检仪器限制使用条件:

Limiting condition of the instrument verified:

注: 1. 本证书检定结果只与受检仪器有关。

2. 未经本中心书面批准, 不得部分复制此证书。

Note: 1. The results relate only to the items verified.

2. This certificate shall not be reproduced except in full, without the written approval of our laboratory.



检定结果 RESULTS OF VERIFICATION

证书编号: SSD20093126
Certification No.

原始记录编号: 220093126
Record No.

第 3 页, 共 3 页
Page of

1. 外观检查: 合格
Check on appearance: pass

2. 声压级 (dB): 见表1
Sound Pressure Level: The value showed in table 1

表1 Table 1

标称值 (dB) Nominal Value	实测值 (dB) Measured Value	允差 (dB) Tolerance	结论 Conclusion	稳定度 (dB) Stabilization	稳定度允差 (dB) Stabilization Tolerance	结论 Conclusion
94	94.06	±0.40	合格(Pass)	0.02	0.10	合格(Pass)
114	114.07	±0.40	合格(Pass)	0.02	0.10	合格(Pass)

3. 频率: 见表2
Frequency: The value showed in table 2

表2 Table 2

标称值 (Hz) Nominal Value	实测值 (Hz) Measured Value	允差 (%) Tolerance	结论 Conclusion
1000	999.84	±1.0	合格(Pass)

4. 总失真: 见表3
Total harmonic distortion: The value showed in table 3

表3 Table 3

声压级 (dB) Sound Pressure Level	失真度 (%) THD (%)	允差 (%) Tolerance	结论 Conclusion
94	0.6	≤3	合格(Pass)
114	0.5	≤3	合格(Pass)

说明(Note)

1. 声压级测量结果扩展不确定度:

Expanded uncertainty of measurement in Sound Pressure Level Calibration:

$U=0.15$ dB, $k=2$

(依据 JJF1059-1999 测量不确定度评定与表示)

(According to JJF1059-1999 Evaluation and Expression of Uncertainty in Measurement)

Appendix C

Calibration Certificates for Measuring Equipments



Report for Calibration of Hand-held Water Quality Meter WQC-24

Calibration Reference No. : GCE/CAL/2009/MW/WQM/C4

Client : ENVIRONMENTAL PIONEER AND SOLUTION LIMITED

Equipment No. : WQC-24 Location : Mui Wo Site

Manufacturer : DKK-TOA Serial No.: 640274

Calibration Date : 24 to 28-12-2009 Due Date : 23-03-2010

Criterion: (Repeatability, Linearity)

pH : Both within ± 0.05 pH
 Dissolved oxygen : Both within ± 0.1 mg/L
 Electric conductivity : Both within $\pm 1\%$ FS
 Turbidity : Repeatability : within $\pm 3\%$ FS
 Temperature : Repeatability $\pm 0.25^\circ\text{C}$; Linearity $\pm 0.5^\circ\text{C}$; (Ambient 5~45°C)

Electric Conductivity (Salinity converted from EC):

(Reference : APHA 20ed 2510 B, ISO 7888 – 1985 (E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Concentration of KCl Standard Solution (M)	Reference conductivity value at 25.0 °C	Indicated value by meter	Linearity (R^2)
0	0.0 mS/m*	0.0 mS/m	1.0000
0.001	14.7 mS/m	15.2 mS/m	
0.005	71.8 mS/m	72.3 mS/m	
0.01	0.141 S/m	0.147 S/m	Acceptance Criterion $R^2 > 0.995$ Within $\pm 1\%$ F.S. against calibration standard value 71.8 mS/m, 0.667 S/m and 5.87 S/m.
0.05	0.667 S/m	0.674 S/m	
0.1	1.29 S/m	1.29 S/m	
0.5	5.87 S/m	5.87 S/m	
Repeatability	1 st time	0.00 , 5.87 S/m	Within $\pm 1\%$ F.S. against average value
	2 nd time	0.00 , 5.87 S/m	
	3 rd time	0.00 , 5.87 S/m	
	0.00 , 5.87 S/m	Ave.: 0.00 , 5.87	

* 1 S/m = 10^4 $\mu\text{mhos/cm}$ = 10^3 mS/m

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Dissolved Oxygen:

(Reference : APHA 20ed 4500-O B&C, ISO 5814:1990(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

DO value evaluated by Iodometric Method (mg/L)		Indicated value by meter (mg/L)	Linearity (R ²)
0.00		0.00	0.9987
3.27		3.36	
5.73		5.80	
8.46		8.50	Acceptance Criterion R ² > 0.995 Within ± 0.1 mg/L against standard value
10.38		10.33	
13.13		13.07	
Repeatability	1 st time	0.00 , 8.52	Within ± 0.1 mg/L against average value
	2 nd time	0.00 , 8.50	
	3 rd time	0.00 , 8.47	
	0.00 , 8.46	Ave.: 0.00 , 0.04	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

pH Value:

(Reference : APHA 20ed 4500-H⁺ B, ISO 10523:1994(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Calibration pH buffer (25°C)	Input value (pH buffer) (25°C)	Indicated pH value by meter (25°C)	Linearity (R ²)
pH = 1.67	1.67	1.70	1.0000
pH = 6.86	4.00	4.02	Acceptance Criterion R ² > 0.995 Within ± 0.05 pH against standard value
pH = 7.42	7.00	7.02	
pH = 9.18	10.00	10.04	
pH = 12.45	12.45	12.47	Within ± 0.05 pH against average value
Repeatability	1 st time	4.02 , 10.03	
	2 nd time	4.02 , 10.04	
	3 rd time	4.01 , 10.04	
	pH 4.00 , 10.00	Ave.: 4.02 , 10.04	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Temperature:

(Reference : APHA 20ed 2550 B, In-house method and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Setting Temperature (°C)	Indicated value by meter (°C)		Linearity (R ²)
5.0	5.3		1.0000
15.0	15.3		
25.0	25.1		Acceptance Criterion R ² > 0.995 Within ± 0.5°C against standard value
35.0	35.2		
45.0	45.3		
55.0	55.2		
Repeatability	1 st time	15.2 , 45.4	Within ± 0.25°C against average value
	2 nd time	15.1 , 45.2	
	3 rd time	15.2 , 45.3	
	15.0 , 45.0	Ave.: 25.2 , 45.3	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.


Turbidity:

(Reference : APHA 20ed 2130 B and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Formazin Standards (NTU)	Indicated value by meter (NTU)		Linearity (R ²)
0.0	0.0		1.0000
20.0	20.5		Acceptance Criterion R ² > 0.995 Within ± 3% F.S. against span calibration value 100.0 and 400.0 NTU
100.0	102.1		
400.0	403.5		
800.0	804.8		
Repeatability	1 st time	0.0 , 804.9	Within ± 3% F.S. against average value
	2 nd time	0.0 , 804.8	
	3 rd time	0.0 , 804.7	
	0.0 , 800.0	Ave.: 0.0 , 804.8	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

Comments : Pass, (comply with the criteria)

Tested by : Ho Tin Kau Certified by : 
 Gu Chin
 Chemist

Checked by : Gu Chin Date : 28-12-2009



Report for Calibration of Hand-held Water Quality Meter WQC-24

Calibration Reference No. : GCE/CAL/2009/MW/WQM/C4

Client : ENVIRONMENTAL PIONEER AND SOLUTION LIMITED

Equipment No. : WQC-24 Location : Mui Wo Site

Manufacturer : DKK-TOA Serial No.: 640274

Calibration Date : 16 to 20-3-2010 Due Date : 15-06-2010

Criterion: (Repeatability, Linearity)

pH : Both within ± 0.05 pH
 Dissolved oxygen : Both within ± 0.1 mg/L
 Electric conductivity : Both within $\pm 1\%$ FS
 Turbidity : Repeatability : within $\pm 3\%$ FS
 Temperature : Repeatability $\pm 0.25^\circ\text{C}$; Linearity $\pm 0.5^\circ\text{C}$; (Ambient $5\sim 45^\circ\text{C}$)

Electric Conductivity (Salinity converted from EC):

(Reference : APHA 20ed 2510 B, ISO 7888 - 1985 (E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Concentration of KCl Standard Solution (M)	Reference conductivity value at 25.0°C	Indicated value by meter	Linearity (R^2)
0	0.0 mS/m*	0.0 mS/m	1.0000
0.001	14.7 mS/m	14.3 mS/m	
0.005	71.8 mS/m	71.2 mS/m	Acceptance Criterion $R^2 > 0.995$ Within $\pm 1\%$ F.S. against calibration standard value 71.8 mS/m, 0.667 S/m and 5.87 S/m.
0.01	0.141 S/m	0.143 S/m	
0.05	0.667 S/m	0.661 S/m	
0.1	1.29 S/m	1.29 S/m	
0.5	5.87 S/m	5.87 S/m	
Repeatability	1 st time	0.00, 5.87 S/m	Within $\pm 1\%$ F.S. against average value
	2 nd time	0.00, 5.87 S/m	
	3 rd time	0.00, 5.87 S/m	
	0.00, 5.87 S/m	Ave.: 0.00, 5.87	

* $1 \text{ S/m} = 10^4 \mu\text{mhos/cm} = 10^3 \text{ mS/m}$

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Dissolved Oxygen:

(Reference : APHA 20ed 4500-O B&C, ISO 5814:1990(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

DO value evaluated by Iodometric Method (mg/L)		Indicated value by meter (mg/L)	Linearity (R ²)
0.00		0.00	0.9999
2.94		3.01	
5.28		5.22	Acceptance Criterion
8.24		8.30	R ² > 0.995 Within ± 0.1 mg/L against standard value
10.56		10.53	
13.22		13.30	
Repeatability	1 st time	0.00 , 8.28	Within ± 0.1 mg/L against average value
	2 nd time	0.00 , 8.30	
	3 rd time	0.00 , 8.31	
	0.00 , 8.24	Ave.: 0.00 , 0.03	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

pH Value:

(Reference : APHA 20ed 4500-H⁺ B, ISO 10523:1994(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Calibration pH buffer (20°C)	Input value (pH buffer) (20°C)	Indicated pH value by meter (20°C)	Linearity (R ²)
pH = 1.67	1.67	1.70	1.0000
pH = 6.88	4.00	4.01	Acceptance Criterion
pH = 7.43	7.00	6.98	R ² > 0.995 Within ± 0.05 pH against standard value
pH = 9.22	10.00	10.03	
pH = 12.64	12.64	12.60	
Repeatability	1 st time	4.01 , 10.03	Within ± 0.05 pH against average value
	2 nd time	4.02 , 10.02	
	3 rd time	4.01 , 10.03	
	pH 4.00 , 10.00	Ave.: 4.01 , 10.03	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Temperature:

(Reference : APHA 20ed 2550 B, In-house method and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Setting Temperature (°C)	Indicated value by meter (°C)		Linearity (R ²)
5.0	4.7		0.9999
15.0	14.8		
25.0	24.8		Acceptance Criterion R ² > 0.995 Within ± 0.5°C against standard value
35.0	34.7		
45.0	45.2		
55.0	55.4		
Repeatability	1 st time	14.8 , 45.1	Within ± 0.25°C against average value
	2 nd time	14.9 , 45.2	
	3 rd time	14.7 , 45.4	
	15.0 , 45.0	Ave.: 14.8 , 45.2	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.


Turbidity:

(Reference : APHA 20ed 2130 B and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Formazin Standards (NTU)	Indicated value by meter (NTU)		Linearity (R ²)
0.0	0.0		1.0000
20.0	19.5		Acceptance Criterion R ² > 0.995 Within ± 3% F.S. against span calibration value 100.0 and 400.0 NTU
100.0	98.7		
400.0	397.9		
800.0	796.8		
Repeatability	1 st time	0.0 , 797.4	Within ± 3% F.S. against average value
	2 nd time	0.0 , 796.0	
	3 rd time	0.0 , 796.9	
	0.0 , 800.0	Ave.: 0.0 , 796.8	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

Comments : Pass, (comply with the criteria)

Tested by : Ho Tin Kau Certified by : 
 Gu Chin
 Chemist

Checked by : Gu Chin Date : 20-3-2010

校正証明書

CALIBRATION CERTIFICATE

品名 PRODUCT NAME : 積分形精密騒音計
Integrating Precision Sound Level Meter
型式 TYPE : 6224
器物番号 PRODUCT NUMBER : 060166
マイク MICROPHONE : 34733
製造者 MANUFACTURER : 株式会社アコー ACO CO., LTD.

※特記事項

[基準器、校正機器のトレーサビリティ証明]

校正に使用した基準器、校正機器は国家基準にトレーサブル
であることを証明致します。

※Special notes

[Traceability certificate of standard instruments and calibration equipment.]

We certify that the standard instruments and calibration equipment
are traceable to the national standards.

平成21年11月16日

November 16, 2009


東京都世田谷区代沢2-6-10
株式会社アコー
代表取締役 寺園信一
2-6-10 Daizawa Setagaya-ku
Tokyo Japan
President : Shinichi Terazono
ACO CO., LTD.

1 試験成績 Test Results

別紙試験成績表添付 Test results are attached as an exhibit.

2 試験条件 Test Requirements

試験日 Test date : 平成21年11月16日 November 16, 2009

温度 Temperature : 22 °C

湿度 Humidity : 73 %

気圧 Barometric pressure : 980 hPa

3 使用機器 Used Equipment

デジタルマルチメーター Digital multimeter VP-2661B No. 780010E122

(有効期間 : 平成21年3月から平成22年3月)

(Effective life : from March, 2009 to March, 2010)

アッテネーター Attenuator STA-115 No. 11075

(有効期間 : 平成21年3月から平成22年3月)

(Effective life : from March, 2009 to March, 2010)

周波数カウンター Frequency counter VP-4545A No. 700008E122

(有効期間 : 平成21年3月から平成22年3月)

(Effective life : from March, 2009 to March, 2010)

オーディオアナライザー Audio Analyzer VP-7721A No. 740039D125

(有効期間 : 平成21年3月から平成22年3月)


(Effective life : from March, 2009 to March, 2010)

コンデンサマイクロホン Condenser Microphone 4160 No. 1248087

(有効期間 : 平成21年2月から平成23年2月)

(Effective life : from February, 2009 to February, 2011)

デジタルマルチメーター、アッテネーター
周波数カウンター、オーディオアナライザー
トレーサビリティ体系図
Traceability Flow Chart
of
Digital Multimeters, Attenuators,
Frequency Counters, and Audio Analyzers

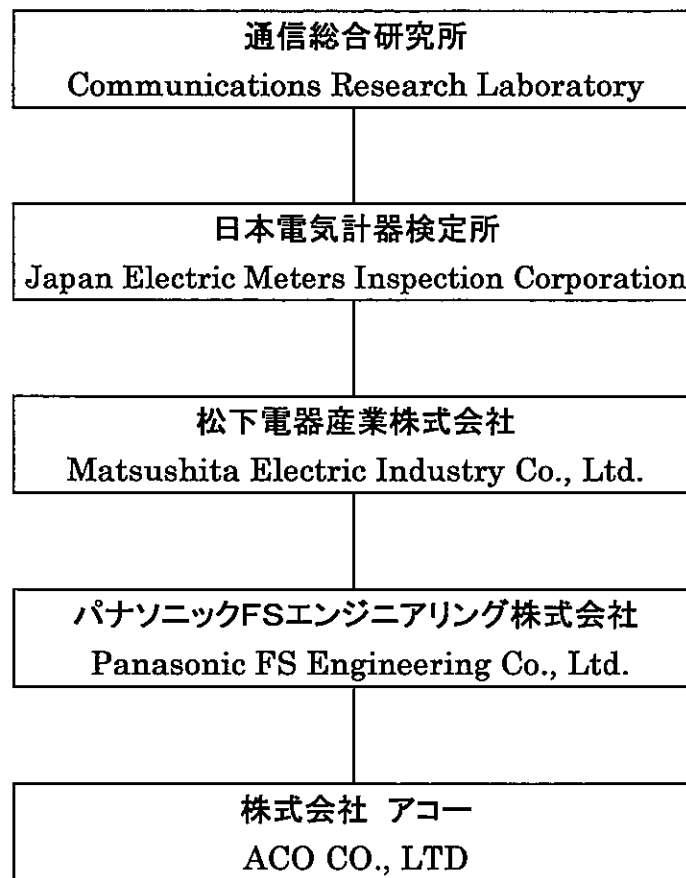

基準静電型マイクロホン
トレーサビリティ体系図
Traceability Flow Chart
of
Standard Electrostatic Microphones



積分形精密騒音計
Integrating Precision Sound Level Meter
TYPE 6224

検査成績書
INSPECTION CERTIFICATE

本体製造番号 060166
Serial No. of body: _____
マイクロホン製造番号 34733
Serial No. of Microphone: _____
Ver:1.6D-06-10

年月日: 平成21年11月16日

Date: November 16, 2009

承認 Approved	点検 Passed	担当 Inspected
J. Yasukage	T. Matsumoto	S. Imoue

株式会社 アコー
ACO CO., LTD.

1. 検査年月日 Inspection Date

平成21年11月16日 November 16, 2009

2. 検査条件 Inspection Condition

- 1) 温度 Temperature : 22 °C
- 2) 湿度 Humidity : 73 %
- 3) 気圧 Barometric pressure : 980 hPa

3. 検査項目及び結果 Inspection Results

1) RANGE 切換誤差検査 The RANGE Shifting Error

RANGE : 20-100dB 70dB 入力基準 ±0.5dB以下

Within ±0.5dB of the value at 70dB input, Range 20-100dB.

RANGE (dB)	入力レベル Input level (dB)	周波数 Frequency (Hz)		
		31.5	1000	8000
20-80	50	-0.1	-0.1	-0.1
20-90	60	0.0	0.0	-0.1
20-100	70	0.0	0.0	0.0
20-110	80	0.0	0.0	0.0
30-120	90	0.0	0.0	0.0
40-130	100	0.0	0.0	0.0
判定	Passed	Pass		

2) 安定性特性検査 Stability Characteristic

RANGE : 20-100dB 1分後基準 ±0.5dB以下

Within ±0.5dB of the value one minute later, Range 20-100dB.

	10分後 ten minutes later
誤差 Error (dB)	0.0
判定 Passed	Pass

3) 目盛誤差特性検査 The Scale Error

RANGE : 20-110dB 65dB入力基準

Error of the value at 65dB input, Range 20-110dB.

入力 Input (dB)	規格 Standard (dB)	周波数 Frequency (Hz)		
		31.5	1000	8000
110	±0.7	0.0	0.0	-0.1
105	±0.7	-0.1	-0.1	-0.1
100	±0.7	-0.1	-0.1	0.0
95	±0.7	-0.1	-0.1	-0.1
90	±0.7	0.1	0.1	0.0
85	±0.7	0.1	0.1	0.0
80	±0.7	0.0	0.0	0.0
75	±0.7	0.0	0.0	0.0
70	±0.7	0.0	0.0	0.0
65	0.0	0.0	0.0	0.0
60	±0.7	0.0	0.0	0.0
55	±0.7	0.0	0.0	-0.1
50	±0.7	0.0	0.0	0.0
45	±0.7	0.0	0.0	0.0
40	±0.7	0.0	0.0	0.0
35	±0.7	0.0	0.0	0.0
30	±0.7	0.0	0.0	0.0
25	±0.7	0.2	0.2	0.2
判定	Passed	Pass		

4) 動特性検査 Dynamic Characteristic

RANGE : 20-100dB 100dB、1kHz 入力基準

When 100dB input, Range 20-100dB at 1kHz.

	規格 Standard	測定値 Measured Value
FAST	-1.0+0.5 -1.0 (dB)	-1.5
SLOW	-4.0±1.0 (dB)	-4.5
判定	Passed	Pass

5) 周波数特性検査 Frequency Response

RANGE : 20-100dB 95dB入力基準(マイクを含む)

When 95dB input, including Microphone value, Range 20-100dB.

周波数 Frequency (Hz)	A特性			C特性			FLAT(Z)特性	許容差 Tolerance
	規格 Standard (dB)	レスポンス Response (dB)	偏差 Deviation (dB)	規格 Standard (dB)	レスポンス Response (dB)	偏差 Deviation (dB)	レスポンス Response (dB)	
20	-50.5	-50.0	0.5	-6.2	-5.8	0.4	-0.9	±3.0
40	-34.6	-34.3	0.3	-2.0	-1.9	0.1	-0.1	±1.5
100	-19.1	-18.9	0.2	-0.3	-0.3	0.0	0.1	±1.0
250	-8.6	-8.4	0.2	0.0	0.0	0.0	0.1	±1.0
500	-3.2	-3.1	0.1	0.0	0.0	0.0	0.1	±1.0
1000	0.0	0.0	0.0	0.0	0.0	0.0	0.1	±1.0
2k	1.2	1.1	-0.1	-0.2	-0.3	-0.1	0.0	±1.0
4k	1.0	0.8	-0.2	-0.8	-0.9	-0.1	0.2	±1.0
5k	0.5	0.5	0.0	-1.3	-1.2	0.1	0.3	±1.5
6.3k	-0.1	-0.1	0.0	-2.0	-1.8	0.2	0.3	+1.5 -2
8k	-1.1	-1.1	0.0	-3.0	-3.5	-0.5	0.3	+1.5 -3
10k	-2.5	-2.5	0.0	-4.4	-4.2	0.2	-0.1	+2 -4
12.5k	-4.3	-3.5	0.8	-6.2	-5.2	1.0	0.2	+3 -6
16k							0.1	
20k							-0.9	
判定 Passed		Pass						

6) 実効値指示誤差検査 Effective Value Error

RANGE : 20-100dB 波高率3のバースト信号に対して1.0dB以内

Within 1.0dB on the Burst signal of the peak factor 3, Range 20-100dB.

周波数 Frequency 2kHz、繰り返し周波数 Repeat frequency 40Hz

実効値指示誤差 Effective value Error (dB)	判定
0.3	Pass

7) 自己雑音特性検査 Self-noise

RANGE : 20-80dB (マイクを含む)


RANGE : 20-80dB (Including Microphone value)

RANGE : 20-80dB (Including Microphone value)	A特性	C特性	FLAT(Z)特性
規格 Standard (dB)	18以下 Below 18	29以下 Below 29	32以下 Below 32
自己雑音 Self-noise (dB)	16.6	22.1	25.3
判定 Passed	Pass		

校正証明書

株式会社 アコー 殿

パナソニック エレクトロニクス株式会社
九州営業所
福岡市博多区博多駅前4丁目9番2号



品 名： デジタルマルチメータ

型 番： VP-2661B

製造会社： 松下通信工業株式会社

管理番号： EMC-10004

製造番号： 780010E122

校正日： 2009年 3月

温 湿 度： 温度 23℃ 湿度 42%


上記の測定器は、当社が運用する標準器により校正した結果、所定の基準に適合していることを証明致します。尚、使用標準器は当社管理規定により管理され、また、トレーサビリティ体系に基づき国家標準（日本電気計器検定所・日本品質保証機構）にトレーサされております。

品 名	型 名	製造会社	製造番号	管理番号	校正有効月
キャリブレータ	5700A	フルク	5440004	KNK1007	2009/06

校正証明書

株式会社 アコー 殿

パナソニック F
九州営業所
福岡市博多区博多駅前4丁目9番2号



品 名 : アッテネータ
型 番 : STA-115
製造会社 : 東京光音電波株式会社
管理番号 : EMC-1 0006
製造番号 : 11075
校正日 : 2009年 3月
温湿度 : 温度 23℃ 湿度 40%


上記の測定器は、当社が運用する標準器により校正した結果、所定の基準に適合していることを証明致します。尚、使用標準器は当社管理規定により管理され、また、トレーサビリティ体系に基づき国家標準（日本電気計器検定所・日本品質保証機構）にトレーサされております。

品 名	型 名	製造会社	製造番号	管理番号	校正有効月
オーディオアライザ	VP-7723A	松下通信工業	101417B122	KNK1006	2009/06

校正証明書

株式会社 アコー 殿

パナソニックエンジニアリング株式会社
九州営業所
福岡市博多区博多駅前2丁目9番2号



品 名 : 周波数カウンタ
型 番 : VP-4545A
製造会社 : 松下通信工業株式会社
管理番号 : EMC-1 0005
製造番号 : 700008E122
校正日 : 2009年 3月
温湿度 : 温度 23℃ 湿度 42%

上記の測定器は、当社が運用する標準器により校正した結果、所定の基準に適合していることを証明致します。尚、使用標準器は当社管理規定により管理され、また、トレーサビリティ体系に基づき国家標準（日本電気計器検定所・日本品質保証機構）にトレースされております。

品 名	型 名	製造会社	製造番号	管理番号	校正有効月
周波数カウンタ	R5363	アドバンテス	40260090	KNK1016	2010/01

校正証明書

株式会社 アコー 殿

パナソニックシステムズリング株式会社
九州営業所
福岡市博多区博多駅前4丁目9番2号

品 名 : オーディオアナライザー

型 番 : VP-7721A

製造会社 : 松下通信工業株式会社

管理番号 : EMC-1 0007

製造番号 : 740039D125

校正日 : 2009年 3月

温湿度 : 温度 23 °C 湿度 40 %

上記の測定器は、当社が運用する標準器により校正した結果、所定の基準に適合していることを証明致します。
尚、使用標準器は当社管理規定により管理され、また、トレーサビリティ体系に基づき国家標準（日本電気計
器検定所・日本品質保証機構）にトレーサされております。

品 名	型 名	製造会社	製造番号	管理番号	校正有効月
キャリブレーション	5700A	フルク	5440004	KNK1007	2009/06
周波数カウンタ	R5363	アドバンテスト	40260090	KNK1016	2010/01
オーディオアナライザー	VP-7723A	松下通信工業	101417B122	KNK1006	2009/06

基準器検査成績書

09SL第4号

騒音基準器

種類 基準静電型マイクロホン

器物番号 1248087 (BK4160)

(1) 音圧感度の周波数特性

(音圧感度レベルは1V/Paを0dBとする)

測定周波数 (Hz)	音圧感度レベル (dB)	測定周波数 (Hz)	音圧感度レベル (dB)
20	-27.1	3000	-26.9
30	-27.2	4000	-26.7
50	-27.2	5000	-26.6
100	-27.3	6000	-26.7
150	-27.2	7000	-27.0
200	-27.3	8000	-27.9
300	-27.3	9000	-29.1
500	-27.3	10000	-30.6
700	-27.3	11000	-32.3
1000	-27.2	12000	-34.1
1500	-27.2	12500	-34.8
2000	-27.1		


(2) 測定条件 温度 23℃、湿度 27%、気圧 1012 hPa、バイアス電圧 200V

(3) 有効期間 平成21年2月17日から平成23年2月16日まで

(4) その他

平成21年2月16日

独立行政法人 産業技術総合研究所





CERTIFICATE OF CALIBRATION

Certificate No.: 10CA0306 01 Page: 1 of 2

Item tested

Description: Acoustical Calibrator (Class 1)
Manufacturer: Castle
Type/Model No.: GA607
Serial/Equipment No.: 039543
Adaptors used: -

Item submitted by

Customer: Geotechnics & Concrete Engineering (H.K.) Ltd.
Address of Customer: 6 Ko Shan Road, Ground FL., Hung Hom, Kowloon, Hong Kong
Request No.: RS/10/023-PO
Date of request: 06-Mar-2010

Date of test: 06-Mar-2010

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	23-Jun-2010	SCL
Preamplifier	B&K 2673	2239857	15-Dec-2010	CEPREI
Measuring amplifier	B&K 2610	2346941	11-Dec-2010	CEPREI
Signal generator	DS 360	61227	22-Jun-2010	CEPREI
Digital multi-meter	34401A	US36087050	03-Dec-2010	CIGISMEC
Audio analyzer	8903B	GB41300350	07-Dec-2010	CEPREI
Universal counter	53132A	MY40003662	23-Jun-2010	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 5 %
Air pressure: 1005 ± 5 hPa


Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:  Date: 09-Mar-2010 Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Appendix D1 Plant species recorded at Pak Ngan Heung River (N)

<i>Species</i>	Habit	Native	Relative	Occurrence	
			Abundance	PNH3	PNH4
<i>Acacia confusa</i>	tree	no	occasional		+
<i>Achyranthes aspera</i>	herb	yes	scarce		+
<i>Acorus gramineus</i>	herb	yes	scarce	+	+
<i>Ageratum conyzoides</i>	herb	yes	scarce		+
<i>Alangium chinensis</i>	tree	yes	scarce		+
<i>Alocasia macrorrhiza</i>	herb	yes	occasional		+
<i>Aporosa dioica</i>	tree	yes	occasional		+
<i>Ardisia crenata</i>	shrub	yes	occasional	+	+
<i>Bamboo</i>	herb	-	scarce	+	
<i>Bidens pilosa</i>	herb	yes	scarce		+
<i>Bischofia javanica</i>	tree	yes	scarce	+	
<i>Celtis sinensis</i>	tree	yes	occasional		+
<i>Centotheca lappacea</i>	grass	yes	scarce		+
<i>Christella parasitica</i>	fern	yes	occasional	+	+
<i>Cleistocalyx operculata</i>	tree	yes	occasional	+	
<i>Commelina sp.</i>	herb	yes	scarce		+
<i>Conyza canadensis</i>	herb	no	scarce		+
<i>Desmos chinensis</i>	shrub	yes	scarce		+
<i>Dimocarpus longan</i>	tree	no	occasional		+
<i>Ficus hispida</i>	tree	yes	common	+	+
<i>Ficus superba</i>	tree	yes	occasional		+
<i>Floscopa scandens</i>	herb	yes	occasional		+
<i>Garcinia oblongifolia</i>	tree	yes	occasional	+	+
<i>Hedychium coronarium</i>	herb	no	scarce		+
<i>Hedyotis auricularia</i>	herb	yes	scarce		+
<i>Hibiscus rosa-sinensis</i>	shrub	no	occasional		+
<i>Homalium cochinchinensis</i>	tree	yes	scarce		+
<i>Liriope spicata</i>	herb	yes	scarce		+
<i>Litsea glutinosa</i>	tree	yes	occasional		+
<i>Litsea rotundifolia</i>	shrub	yes	scarce	+	
<i>Lophatherum gracile</i>	grass	yes	scarce	+	+
<i>Ludwigia perennis</i>	herb	yes	scarce		+
<i>Lygodium japonicum</i>	fern	yes	scarce		+

<i>Species</i>	Habit	Native	Relative	Occurrence	
			Abundance	PNH3	PNH4
<i>Macaranga tanarius</i>	tree	yes	occasional	+	+
<i>Mallotus paniculatus</i>	tree	yes	scarce	+	
<i>Melastoma sanguineum</i>	shrub	yes	scarce		+
<i>Microcos paniculata</i>	tree	yes	scarce		+
<i>Microstegium ciliatum</i>	grass	yes	common		+
<i>Mikania micrantha</i>	climber	no	common	+	+
<i>Musa paradisiaca</i>	tree	no	scarce	+	
<i>Mussaenda erosa</i>	shrub	yes	scarce	+	
<i>Neyraudia reynaudiana</i>	grass	yes	occasional		+
<i>Panicum maximum</i>	grass	no	common		+
<i>Phyllanthus urinaria</i>	herb	yes	scarce		+
<i>Pilea microphylla</i>	herb	no	occasional		+
<i>Pistia stratiotes</i>	herb	yes	scarce		+
<i>Plantago major</i>	herb	yes	scarce		+
<i>Pogonatherum crinitum</i>	grass	yes	scarce		+
<i>Polygonum chinense</i>	herb	yes	occasional	+	
<i>Psychotria asiatica</i>	shrub	yes	common	+	+
<i>Pueraria phaseoloides</i>	climber	yes	occasional	+	+
<i>Sageretia thea</i>	climber	yes	occasional		+
<i>Scherfflera heptaphylla</i>	tree	yes	scarce	+	
<i>Scoparia dulcis</i>	herb	yes	herb		+
<i>Severinia buxifolia</i>	shrub	yes	scarce		+
<i>Sporobolus fertilis</i>	grass	yes	scarce		+
<i>Stephania longa</i>	climber	yes	scarce		+
<i>Sterculia lanceolata</i>	tree	yes	common	+	+
<i>Synedrella nodiflora</i>	herb	yes	scarce		+
<i>Syngonium podophyllum</i>	climber	no	occasional	+	
<i>Syzygium jambos</i>	tree	no	common	+	+
<i>Syzygium levinei</i>	tree	yes	scarce	+	
<i>Urena lobata</i>	tree	yes	scarce		+
<i>Uvaria microcarpa</i>	shrub	yes	scarce	+	
<i>Vernonia cinera</i>	herb	yes	scarce		+
<i>Wedelia triloba</i>	climber	no	scarce	+	
<i>Zanthoxylum avicennae</i>	tree	yes	scarce		+

Appendix D2 Plant species recorded at Pak Ngan Heung River (S)

Species	Habit	Native	Relative	Occurrence	
			Abundance	PNH1	PNH2
<i>Celtis sinensis</i>	tree	yes	occasional		+
<i>Clerodendrum inerme</i>	tree	yes	occasional	+	+
<i>Ficus microcarpa</i>	tree	yes	scarce		+
<i>Ficus superba</i>	tree	yes	occasional		+
<i>Ipomoea cairica</i>	climber	yes	occasional		+
<i>Kandelia obovata</i>	tree	yes	scarce	+	
<i>Lantana camara</i>	shrub	no	scarce		+
<i>Panicum maximum</i>	grass	no	common	+	+

Appendix D3 Plant species recorded at Luk Tei Tong River

			Relative	Occurrence				
Species	Habit	Native	Abundance	LLT1	LLT2	LLT3	LLT4	LLT5
<i>Kandelia obovata</i>	tree	yes	scarce		+			
<i>Panicum maximum</i>	grass	no	scarce	+				
<i>Rhynchelytrum repens</i>	grass	no	scarce	+				
<i>Saccharum arundinaceum</i>	grass	yes	scarce	+				

Appendix D4

Ecological Water Monitoring Results (on-site measurements)

Environmental Pioneers & Solutions Limited
Ecological Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 1/3/2010

Weather Condition: Sunny

Monitoring Location	WE1			WE2			WE3			WE4			WE5			WE6		
Time (hhmm)	1115			1100			1235			1245			1255			1140		
Tide Mode	ebb			ebb			ebb			ebb			ebb			ebb		
River Condition	Normal			Normal			Muddy			Muddy			Normal			Normal		
Water Depth (m)	< 1.0			< 1.0			< 1.0			< 1.0			< 1.0			< 1.0		
pH value	7.11			7.61			7.61			7.01			7.22			6.78		
Temperature (oC)	22.5			22.4			21.9			22.5			22.5			21.5		
Salinity (ppt)	0.0			0.4			2.9			12.5			4.2			0.0		
Conductivity (ms/m)	15.8			100.0			532.0			2050.0			755.0			6.4		
Water flow (m/s)	0.010			0.020			0.020			0.010			0.020			0.010		
Turbidity (NTU)	0.0	0.0	Average	4.3	4.2	Average	13.8	13.9	Average	9.3	9.4	Average	4.6	4.4	Average	0.0	0.0	Average
			0.00			4.25			13.85			9.4			4.50			0.0
DO (mg/l)	6.73	6.74	Average	7.51	7.49	Average	7.56	7.57	Average	6.10	6.12	Average	8.10	8.09	Average	7.46	7.46	Average
			6.74			7.50			7.57			6.11			8.10			7.46
DO Saturation (%)	78	78	Average	87	87	Average	88	88	Average	71	71	Average	94	94	Average	85	85	Average
			78			87			88			71			94			85

Name
Prepared By: Jimmy Cheng

Signature


Date
1/3/2010

remark or observation: _____

Appendix D5

Ecological Water Monitoring Results (lab report)



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300142 Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 02-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	503	499	0.8	24.3
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID		WE1	WE1 Duplicate	WE2	WE2 Duplicate	WE3	WE3 Duplicate		
	Sampling Date/Time		01 Mar 2010 / 11:15		01 Mar 2010 / 11:00		01 Mar 2010 / 12:35			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	3.0	3.2	11.6	11.9		

TEST RESULTS	Sample ID		WE4	WE4 Duplicate	WE5	WE5 Duplicate	WE6	WE6 Duplicate		
	Sampling Date/Time		01 Mar 2010 / 12:45		01 Mar 2010 / 12:55		01 Mar 2010 / 11:40			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	12.4	12.1	9.6	10.0	1.5	1.6		

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : Location M1 & WE3 and Location M3 & WE4 are the same location.

----- End -----

Tested By : K.L FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC100300516

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Contract No.* : -- Date Completed : 12-03-2010

GCE Serial No. : WQM032010 Sampling Date* : 01-03-2010 / 11:15 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE1

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.04
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.19
Phosphorus mg/L	APHA 20ed 4500-P D	0.05
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	< 1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE1.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 
 Name : Gu Chin
 Post : Chemist

Checked By : Gu Chin



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC100300524 Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Contract No.* : -- Date Completed : 12-03-2010

GCE Serial No. : WQM032010 Sampling Date* : 01-03-2010 / 11:15 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE1 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.04
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.18
Phosphorus mg/L	APHA 20ed 4500-P D	0.05
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	< 1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE1.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan Certified By : 
 Name : Gu Chin
 Checked By : Gu Chin Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC100300532

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 11:00

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE2

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.09
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.21
Phosphorus mg/L	APHA 20ed 4500-P D	0.12
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	5
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE2.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By :

Name :

Gu Chin

Checked By : Gu Chin

Post :

Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC100300540

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 11:00

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE2 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.10
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.21
Phosphorus mg/L	APHA 20ed 4500-P D	0.13
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	5
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE2.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By :

Name

Gu Chin

Checked By : Gu Chin

Post

Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300558

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Contract No.* : -- Date Completed : 12-03-2010

GCE Serial No. : WQM032010 Sampling Date* : 01-03-2010 / 12:35 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE3

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.16
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.35
Phosphorus mg/L	APHA 20ed 4500-P D	0.12
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	4
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE3.


----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By

Name

Post

: 
 : Gu Chin
 : Chemist

Checked By : Gu Chin



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300566

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 12:35

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE3 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.15
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.36
Phosphorus mg/L	APHA 20ed 4500-P D	0.12
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	4
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE3.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300574

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 12:45

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE4

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU	APHA 20ed 2120 B
Turbidity	NTU	APHA 20ed 2130 B
Conductivity at 25°C	µS/cm	APHA 20ed 2510 B.
Salinity	g/L	APHA 20ed 2520 B
Nitrogen (Ammonia)	APHA 20ed 4500-NH ₃ D	0.86
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate)	mg/L	APHA 20ed 4500-NO ₃ ⁻ E
Phosphorus	mg/L	APHA 20ed 4500-P D
Biochemical Oxygen Demand (BOD ₅)	mg/L	APHA 20ed 5210 B
Chemical Oxygen Demand (COD)	mg/L	APHA 20ed 5220 D
Total Suspended Solid	mg/L	APHA 20ed 2540 D

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE4.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 

Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300582

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 12:45

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE4 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU	APHA 20ed 2120 B
Turbidity	NTU	APHA 20ed 2130 B
Conductivity at 25°C	µS/cm	APHA 20ed 2510 B
Salinity	g/L	APHA 20ed 2520 B
Nitrogen (Ammonia)	mg/L	APHA 20ed 4500-NH ₃ D
		APHA 20ed 4500-NH ₃ E
		APHA 18ed 4500-NH ₃ C
Nitrogen (Nitrate)	mg/L	APHA 20ed 4500-NO ₃ ⁻ E
Phosphorus	mg/L	APHA 20ed 4500-P D
Biochemical Oxygen Demand (BOD ₅)	mg/L	APHA 20ed 5210 B
Chemical Oxygen Demand (COD)	mg/L	APHA 20ed 5220 D
Total Suspended Solid	mg/L	APHA 20ed 2540 D

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE4.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 

Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300590

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Contract No.* : -- Date Completed : 12-03-2010

GCE Serial No. : WQM032010 Sampling Date* : 01-03-2010 / 12:55 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE5

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.70
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.22
Phosphorus mg/L	APHA 20ed 4500-P D	0.39
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	3
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE5.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 
 Name : Gu Chin
 Post : Chemist

Checked By : Gu Chin



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300605

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 12:55

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE5 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU	APHA 20ed 2120 B
Turbidity	NTU	APHA 20ed 2130 B
Conductivity at 25°C	µS/cm	APHA 20ed 2510 B
Salinity	g/L	APHA 20ed 2520 B
Nitrogen (Ammonia)	APHA 20ed 4500-NH ₃ D	1.69
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate)	mg/L	APHA 20ed 4500-NO ₃ ⁻ E
Phosphorus	mg/L	APHA 20ed 4500-P D
Biochemical Oxygen Demand (BOD ₅)	mg/L	APHA 20ed 5210 B
Chemical Oxygen Demand (COD)	mg/L	APHA 20ed 5220 D
Total Suspended Solid	mg/L	APHA 20ed 2540 D

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE5.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 

Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC100300613

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Contract No.* : -- Date Completed : 12-03-2010

GCE Serial No. : WQM032010 Sampling Date* : 01-03-2010 / 11:40 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE6

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.03
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.13
Phosphorus mg/L	APHA 20ed 4500-P D	0.04
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE6.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By : 
 Name : Gu Chin
 Post : Chemist

Checked By : Gu Chin



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC100300621

Date of Issue : 31-03-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 01-03-2010

W.O. No.* : --

Contract No.* : --

Date Completed : 12-03-2010

GCE Serial No. : WQM032010

Sampling Date* : 01-03-2010 / 11:40

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE6 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU APHA 20ed 2120 B	--
Turbidity	NTU APHA 20ed 2130 B	--
Conductivity at 25°C	µS/cm APHA 20ed 2510 B	--
Salinity	g/L APHA 20ed 2520 B	--
Nitrogen (Ammonia)	mg/L APHA 20ed 4500-NH ₃ D	0.02
	mg/L APHA 20ed 4500-NH ₃ E	--
	mg/L APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate)	mg/L APHA 20ed 4500-NO ₃ ⁻ E	0.12
Phosphorus	mg/L APHA 20ed 4500-P D	0.04
Biochemical Oxygen Demand (BOD ₅)	mg/L APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD)	mg/L APHA 20ed 5220 D	--
Total Suspended Solid	mg/L APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 01 March 2010.

REMARKS : Sample Location WE6.

----- End -----

Tested By : T.W. Lam, K.L. Fong, S.F. Kan

Certified By

Name

Gu Chin

Checked By : Gu Chin

Post

Chemist

Appendix E

Construction Noise Monitoring Data Sheet



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		5/3/2010	
Measurement Start Time (hhmm)		14:20	13:40
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.7	1.2
Measurement Results	L90 (dB(A))	48.0	55.8
	L10 (dB(A))	58.6	65.3
	Leq (dB(A))	56.9	64.7
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction works are being carried out during measurement.	1. Excavator noise 2. Power generator noise 3. Construction trucks noise
Other Noise Source(s) During Monitoring		1. Public noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

5/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		5/3/2010	
Measurement Start Time (hhmm)		13:00	11:35
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.9	1.2
Measurement Results	L90 (dB(A))	47.1	43.7
	L10 (dB(A))	57.2	53.7
	Leq (dB(A))	54.8	52.9
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		1. Excavator noise 2. Power generator noise	No construction works are being carried out during measurement.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise (bicycle)	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

5/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		12/3/2010	
Measurement Start Time (hhmm)		14:50	14:15
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.2	0.3
Measurement Results	L90 (dB(A))	49.1	50.6
	L10 (dB(A))	54.9	64.3
	Leq (dB(A))	53.1	62.1
Weather condition:		Cloudy	
Major Construction Noise Source(s) During Monitoring		No construction works are being carried out during measurement.	1. Excavator noise 2. Power generator noise 3. Construction trucks noise
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

12/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		12/3/2010	
Measurement Start Time (hhmm)		13:40	13:05
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.3	0.4
Measurement Results	L90 (dB(A))	46.7	45.1
	L10 (dB(A))	54.2	51.3
	Leq (dB(A))	52.3	49.4
Weather condition:		Cloudy	
Major Construction Noise Source(s) During Monitoring		1. Excavator noise 2. Construction trucks noise	1. Excavator noise
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise (bicycle)	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

12/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		19/3/2010	
Measurement Start Time (hhmm)		13:00	13:35
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.8	1.1
Measurement Results	L90 (dB(A))	47.3	56.3
	L10 (dB(A))	61.1	65.1
	Leq (dB(A))	57.8	62.3
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction works are being carried out during measurement.	1. Excavator noise 2. Construction trucks noise 3. Power generator noise
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise (bicycle)	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

19/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		19/3/2010	
Measurement Start Time (hhmm)		11:55	11:20
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.6	0.7
Measurement Results	L90 (dB(A))	44.1	42.0
	L10 (dB(A))	54.7	52.8
	Leq (dB(A))	51.6	51.5
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		1. Excavator noise 2. Construction truck noise	No construction works are being carried out during measurement.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise (bicycle)	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

19/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		26/3/2010	
Measurement Start Time (hhmm)		14:10	14:45
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.7	0.8
Measurement Results	L90 (dB(A))	50.2	48.5
	L10 (dB(A))	59.8	58.4
	Leq (dB(A))	57.3	56.9
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction works are being carried out during measurement.	1. Excavator noise 2. Construction trucks noise 3. Power generator noise
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

26/3/2010



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		26/3/2010	
Measurement Start Time (hhmm)		13:35	13:00
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.9	1.1
Measurement Results	L90 (dB(A))	47.1	44.6
	L10 (dB(A))	56.9	53.4
	Leq (dB(A))	55.3	51.2
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		1. Excavator noise	No construction works are being carried out during measurement.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise (bicycle)	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by:

Jimmy Cheng

26/3/2010

Appendix F1

Water Quality

Monitoring Data Sheet

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 1/3/2010

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1235			1240			1245			1225			1115			1130			1255		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	7.60			7.64			7.01			6.97			7.14			6.69			7.18		
Temperature (oC)	21.9			21.6			22.5			22.0			22.5			21.3			22.6		
Salinity (ppt)	2.9			0.5			12.5			15.9			0.0			0.0			2.3		
Turbidity (NTU)	13.9	13.8	Average 13.9	0.0	0.0	Average 0.0	9.3	9.4	Average 9.4	8.2	8.1	Average 8.2	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	6.6	6.4	Average 6.5
DO (mg/l)	7.56	7.57	Average 7.57	9.64	9.63	Average 9.64	6.10	6.12	Average 6.11	8.12	8.12	Average 8.12	6.78	6.77	Average 6.78	8.86	8.85	Average 8.86	8.18	8.17	Average 8.18
DO Saturation (%)	88	88	Average 88	110	110	Average 110	71	71	Average 71	93	93	Average 93	78	78	Average 78	101	101	Average 101	95	95	Average 95

Name
Prepared By: Jimmy Cheng

Signature


Date
1/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 3/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1420			1425			1430			1410			1440			1450			1500		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			Muddy			Muddy			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	7.88			7.92			7.27			7.67			7.63			7.21			6.85		
Temperature (oC)	24.4			25.1			25.3			25.2			24.6			24.4			26.3		
Salinity (ppt)	3.3			1.1			15.3			17.6			0.0			0.0			2.8		
Turbidity (NTU)	12.4	12.4	Average	0.0	0.0	Average	194.6	194.4	Average	55.8	55.7	Average	1.8	1.9	Average	10.4	10.2	Average	12.6	12.6	Average
			12.4			0.0			194.5			55.8			1.9			10.3			12.6
DO (mg/l)	8.93	8.92	Average	10.47	10.45	Average	9.78	9.78	Average	10.23	10.22	Average	9.31	9.30	Average	9.57	9.57	Average	9.96	9.98	Average
			8.93			10.46			9.78			10.23			9.31			9.57			9.97
DO Saturation (%)	107	107	Average	127	127	Average	119	119	Average	125	125	Average	113	113	Average	115	115	Average	124	124	Average
			107			127			119			125			113			115			124

Name
Prepared By: Jimmy Cheng

Signature


Date
3/3/2010

remark or observation: Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 0403/2010

Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)							1430			1420									1440		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			Muddy			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.4			<1			<1			<1		
pH value							7.78			7.89									7.47		
Temperature (oC)							25.4			25.0									26.6		
Salinity (ppt)							17.6			16.2									11.0		
Turbidity (NTU)			Average			Average	69.7	69.6	Average	10.2	10.1	Average			Average			Average	17.5	17.7	Average
			#DIV/0!			#DIV/0!			69.7			10.2			#DIV/0!			#DIV/0!			17.6
DO (mg/l)			Average			Average	9.43	9.41	Average	10.12	10.13	Average			Average			Average	9.74	9.73	Average
			#DIV/0!			#DIV/0!			9.42			10.13			#DIV/0!			#DIV/0!			9.74
DO Saturation (%)			Average			Average	115	115	Average	124	124	Average			Average			Average	121	121	Average
			#DIV/0!			#DIV/0!			115			124			#DIV/0!			#DIV/0!			121

Name
Prepared By: Jimmy Cheng

Signature


Date
0403/2010

remark or observation: Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 5/3/2010

Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1550			1545			1540			1600			1500			1510			1525		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	Muddy			normal			Muddy			Muddy			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.4			<1			<1			<1		
pH value	7.90			7.92			7.49			7.84			7.74			7.24			6.79		
Temperature (oC)	25.1			26.0			26.3			25.9			25.1			25.2			26.9		
Salinity (ppt)	3.5			1.7			17.0			15.8			0.0			0.0			11.4		
Turbidity (NTU)	23.4	23.3	Average 23.4	3.1	3.1	Average 3.1	89.5	89.3	Average 89.4	29.7	29.6	Average 29.7	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	28.9	28.8	Average 28.9
DO (mg/l)	9.26	9.27	Average 9.27	10.79	10.78	Average 10.79	10.27	10.26	Average 10.27	10.55	10.53	Average 10.54	8.79	8.77	Average 8.78	9.49	9.48	Average 9.49	10.11	10.10	Average 10.11
DO Saturation (%)	112	112	Average 112	133	133	Average 133	127	127	Average 127	130	130	Average 130	107	107	Average 107	115	115	Average 115	126	126	Average 126

Name
Prepared By: Jimmy Cheng

Signature


Date
5/3/2010

remark or observation: Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 6/3/2010

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1520						1530			1515			1445						1455		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	Muddy			normal			Muddy			Muddy			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.5			<1			<1			<1		
pH value	7.98						9.98			7.81			7.41						6.94		
Temperature (oC)	25.2						25.9			26.2			25.5						26.6		
Salinity (ppt)	7.7						16.6			18.9			0.0						15.1		
Turbidity (NTU)	19.8	19.7	Average			Average	552.7	552.5	Average	35.6	35.4	Average	0.0	0.0	Average			Average	20.2	20.1	Average
			19.8			#DIV/0!			552.6			35.5			0.0			#DIV/0!			20.2
DO (mg/l)	9.27	9.26	Average			Average	9.42	9.42	Average	10.13	10.12	Average	8.31	8.33	Average			Average	9.17	9.18	Average
			9.27			#DIV/0!			9.42			10.13			8.32			#DIV/0!			9.18
DO Saturation (%)	114	114	Average			Average	117	117	Average	125	125	Average	102	102	Average			Average	115	115	Average
			114			#DIV/0!			117			125			102			#DIV/0!			115

Name
Prepared By: Jimmy Cheng

Signature


Date
6/3/2010

remark or observation: Surface run-off and disturbance of sediment occurred due to excavation activities at LTT river

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 8/3/2010

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1525						1535			1515			1550						1600		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.8			<1			<1			<1		
pH value	7.93						7.91			8.03			7.36						7.56		
Temperature (oC)	19.8						20.2			19.4			18.6						18.4		
Salinity (ppt)	21.6						23.2			16.9			0.4						0.0		
Turbidity (NTU)	9.3	9.4	Average			Average	3.3	3.2	Average	2.6	2.4	Average	0.0	0.0	Average			Average	6.8	6.9	Average
			9.4			#DIV/0!			3.3			2.5			0.0			#DIV/0!			6.9
DO (mg/l)	8.24	8.26	Average			Average	7.56	7.57	Average	8.05	8.06	Average	7.54	7.53	Average			Average	7.30	7.31	Average
			8.25			#DIV/0!			7.57			8.06			7.54			#DIV/0!			7.31
DO Saturation (%)	90	90	Average			Average	83	83	Average	88	88	Average	81	81	Average			Average	79	79	Average
			90			#DIV/0!			83			88			81			#DIV/0!			79

Name
Prepared By: Jimmy Cheng

Signature


Date
8/3/2010

remark or observation: High water level during sampling

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 11/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1055			1100			1105			1045			1115			1125			1135		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			Muddy			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	8.47			7.68			7.53			8.17			7.54			7.87			7.43		
Temperature (oC)	17.3			17.3			18.6			18.4			14.6			18.5			19.5		
Salinity (ppt)	1.1			0.1			11.3			18.5			0.0			0.0			0.7		
Turbidity (NTU)	7.6	7.8	Average 7.7	0.6	0.7	Average 0.7	21.4	21.3	Average 21.4	8.4	8.3	Average 8.4	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	2.4	2.5	Average 2.5
DO (mg/l)	9.12	9.11	Average 9.12	10.61	10.59	Average 10.60	9.73	9.71	Average 9.72	9.47	9.47	Average 9.47	9.66	9.65	Average 9.66	9.72	9.71	Average 9.72	8.92	8.92	Average 8.92
DO Saturation (%)	95	95	Average 95	110	110	Average 110	104	104	Average 104	101	101	Average 101	95	95	Average 95	104	104	Average 104	98	98	Average 98

Name
Prepared By: Jimmy Cheng

Signature


Date
11/3/2010

remark or observation: No silted water leakage observed at location M3, but
muddy water is still observed due to pumping at silted
water into water to river earier in LLT river.

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 12/3/2010

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1145			1150			1200			1135			1210			1220			1230		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			Muddy			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	8.03			7.71			7.19			7.92			7.65			7.42			7.13		
Temperature (oC)	17.5			18.0			18.7			18.5			18.1			18.7			18.8		
Salinity (ppt)	1.5			0.0			7.5			18.8			0.0			0.0			2.1		
Turbidity (NTU)	3.0	2.9	Average 3.0	0.0	0.0	Average 0.0	18.4	18.3	Average 18.4	5.4	5.5	Average 5.5	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	4.5	4.4	Average 4.5
DO (mg/l)	8.48	8.49	Average 8.49	9.95	9.97	Average 9.96	7.37	7.35	Average 7.36	8.83	8.82	Average 8.83	8.60	8.61	Average 8.61	9.21	9.21	Average 9.21	7.43	7.44	Average 7.44
DO Saturation (%)	89	89	Average 89	106	106	Average 106	78	78	Average 78	96	96	Average 96	93	93	Average 93	99	99	Average 99	79	79	Average 79

Name
Prepared By: Jimmy Cheng

Signature


Date
12/3/2010

remark or observation: No silted water discharged and excavation works were observed in the water, but the water in location M3 is muddy due to accumulation of silted water at the bottom of the river.

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 13/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1145			1150			1200			1140			1210			1220			1230		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			< 1			< 1			< 1			< 1		
pH value	8.26			8.01			7.21			7.80			7.62			7.51			7.08		
Temperature (oC)	18.2			19.2			19.8			19.4			17.7			19.6			19.9		
Salinity (ppt)	1.0			0.2			7.9			17.8			0.3			0.0			0.7		
Turbidity (NTU)	5.3	5.3	Average 5.3	0.0	0.0	Average 0.0	7.9	7.8	Average 7.9	6.9	6.8	Average 6.9	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.9	0.8	Average 0.9
DO (mg/l)	8.85	8.84	Average 8.85	10.32	10.34	Average 10.33	7.39	7.38	Average 7.39	8.80	8.79	Average 8.80	8.42	8.41	Average 8.42	10.04	10.03	Average 10.04	9.35	9.34	Average 9.35
DO Saturation (%)	94	94	Average 94	112	112	Average 112	82	82	Average 82	96	96	Average 96	89	89	Average 89	110	110	Average 110	102	102	Average 102

Name
Prepared By: Jimmy Cheng

Signature


Date
13/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 15/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1220			1225			1230			1210			1240			1250			1300		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	8.04			7.76			7.25			7.85			7.72			7.24			7.02		
Temperature (oC)	20.8			21.6			22.8			21.9			21.4			22.7			23.2		
Salinity (ppt)	1.0			0.2			9.3			12.8			0.0			0.0			0.9		
Turbidity (NTU)	5.6	5.5	Average 5.6	0.0	0.0	Average 0.0	10.8	10.7	Average 10.8	6.7	6.8	Average 6.8	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	1.9	1.8	Average 1.9
DO (mg/l)	7.72	7.71	Average 7.72	10.51	10.52	Average 10.52	9.09	9.08	Average 9.09	9.82	9.81	Average 9.82	8.53	8.53	Average 8.53	9.91	9.89	Average 9.90	10.56	10.55	Average 10.56
DO Saturation (%)	87	87	Average 87	120	120	Average 120	106	106	Average 106	112	112	Average 112	96	96	Average 96	115	115	Average 115	124	124	Average 124

Name
Prepared By: Jimmy Cheng

Signature


Date
15/3/2010

remark or
observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 17/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1345			1350			1400			1340			1410			1420			1430		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	8.24			8.06			7.60			7.96			7.81			7.23			7.03		
Temperature (oC)	21.1			21.3			21.6			21.4			20.0			21.7			22.3		
Salinity (ppt)	2.0			1.0			15.2			17.4			0.0			0.0			2.1		
Turbidity (NTU)	6.9	7.0	Average 7.0	0.0	0.0	Average 0.0	7.6	7.5	Average 7.6	9.7	9.5	Average 9.6	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	3.9	3.8	Average 3.9
DO (mg/l)	8.83	8.81	Average 8.82	11.30	11.29	Average 11.30	11.08	11.06	Average 11.07	10.61	10.60	Average 10.61	8.76	8.77	Average 8.77	9.63	9.61	Average 9.62	8.55	8.54	Average 8.55
DO Saturation (%)	99	99	Average 99	128	128	Average 128	126	126	Average 126	120	120	Average 120	97	97	Average 97	110	110	Average 110	97	97	Average 97

Name
Prepared By: Jimmy Cheng

Signature


Date
17/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 19/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1425			1435			1440			1415			1450			1500			1510		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			1.2			< 1			< 1			< 1		
pH value	8.03			8.05			7.78			8.24			8.04			7.52			7.11		
Temperature (oC)	24.1			25.1			25.4			25.2			22.1			24.7			25.8		
Salinity (ppt)	2.0			1.1			19.8			20.5			0.0			0.0			2.2		
Turbidity (NTU)	19.3	19.2	Average 19.3	3.1	3.2	Average 3.2	18.8	18.6	Average 18.7	7.1	6.9	Average 7.0	0.6	0.7	Average 0.7	0.0	0.0	Average 0.0	26.6	26.5	Average 26.6
DO (mg/l)	8.26	8.25	Average 8.26	12.06	12.05	Average 12.06	12.87	12.85	Average 12.86	12.08	12.06	Average 12.07	10.78	10.77	Average 10.78	9.59	9.58	Average 9.59	10.99	10.98	Average 10.99
DO Saturation (%)	99	99	Average 99	147	147	Average 147	156	156	Average 156	147	147	Average 147	124	124	Average 124	115	115	Average 115	134	134	Average 134

Name
Prepared By: Jimmy Cheng

Signature


Date
19/3/2010

Disturbance of sediment occurred due to excavation
 remark or observation: activities at PNH river

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 20/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1425						1430						1440						1450		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.6			<1			<1			<1		
pH value	7.76						7.73						8.07						7.16		
Temperature (oC)	21.9						23.2						21.9						23.7		
Salinity (ppt)	2.9						20.5						0.0						4.2		
Turbidity (NTU)	14.4	14.6	Average			Average	7.3	7.2	Average			Average	0.0	0.0	Average			Average	6.4	6.3	Average
			14.5			#DIV/0!			7.3			#DIV/0!			0.0			#DIV/0!			6.4
DO (mg/l)	8.58	8.57	Average			Average	10.81	10.80	Average			Average	9.37	9.39	Average			Average	11.25	11.26	Average
			8.58			#DIV/0!			10.81			#DIV/0!			9.38			#DIV/0!			11.26
DO Saturation (%)	97	97	Average			Average	127	127	Average			Average	107	107	Average			Average	132	132	Average
			97			#DIV/0!			127			#DIV/0!			107			#DIV/0!			132

Name
Prepared By: Jimmy Cheng

Signature


Date
20/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 22/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1615			1610			1605			1625			1530			1540			1550		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.6			<1			<1			<1		
pH value	7.96			8.11			7.68			7.99			7.23			6.87			6.86		
Temperature (oC)	23.4			24.4			25.0			24.6			23.2			23.7			24.9		
Salinity (ppt)	12.7			8.5			20.9			19.6			0.0			0.0			18.3		
Turbidity (NTU)	130.8	130.6	Average	0.0	0.0	Average	6.5	6.3	Average	10.9	10.8	Average	0.0	0.0	Average	0.0	0.0	Average	14.6	14.4	Average
			130.7			0.0			6.4			10.9			0.0			0.0			14.5
DO (mg/l)	9.87	9.89	Average	12.88	12.87	Average	11.08	11.06	Average	11.04	11.03	Average	10.64	10.62	Average	9.84	9.85	Average	10.55	10.54	Average
			9.88			12.88			11.07			11.04			10.63			9.85			10.55
DO Saturation (%)	116	116	Average	149	149	Average	134	134	Average	133	133	Average	124	124	Average	115	115	Average	128	128	Average
			116			149			134			133			124			115			128

Name
Prepared By: Jimmy Cheng

Signature


Date
22/3/2010

remark or observation: Soil runoff arising from earth movement and excavation
works from site retaining wall C

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 23/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1620												1610								
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	Muddy			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			< 1			< 1			1.6			< 1			< 1			< 1		
pH value	8.43												7.67								
Temperature (oC)	23.5												23.2								
Salinity (ppt)	13.5												0.0								
Turbidity (NTU)	27.4	27.2	Average			Average			Average			Average	0.0	0.0	Average			Average			Average
			27.3			#DIV/0!			#DIV/0!			#DIV/0!			0.0			#DIV/0!			#DIV/0!
DO (mg/l)	9.38	9.39	Average			Average			Average			Average	8.75	8.74	Average			Average			Average
			9.39			#DIV/0!			#DIV/0!			#DIV/0!			8.75			#DIV/0!			#DIV/0!
DO Saturation (%)	111	111	Average			Average			Average			Average	104	104	Average			Average			Average
			111			#DIV/0!			#DIV/0!			#DIV/0!			104			#DIV/0!			#DIV/0!

Name
Prepared By: Jimmy Cheng

Signature


Date
23/3/2010

remark or observation: Soil runoff arising from earth movement and excavation
works from site retaining wall C

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 24/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1620												1610								
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			1.6			< 1			< 1			< 1		
pH value	7.95												7.71								
Temperature (oC)	23.6												23.1								
Salinity (ppt)	18.3												0.0								
Turbidity (NTU)	12.4	12.2	Average			Average			Average			Average	0.0	0.0	Average			Average			Average
			12.3			#DIV/0!			#DIV/0!			#DIV/0!			0.0			#DIV/0!			#DIV/0!
DO (mg/l)	8.17	8.16	Average			Average			Average			Average	8.13	8.14	Average			Average			Average
			8.17			#DIV/0!			#DIV/0!			#DIV/0!			8.14			#DIV/0!			#DIV/0!
DO Saturation (%)	96	96	Average			Average			Average			Average	95	95	Average			Average			Average
			96			#DIV/0!			#DIV/0!			#DIV/0!			95			#DIV/0!			#DIV/0!

Name
Prepared By: Jimmy Cheng

Signature


Date
24/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 26/3/2010

Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1045			1050			1130			1035			1110			1120			1100		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	8.32			8.44			8.08			7.99			7.72			7.31			7.64		
Temperature (oC)	20.2			18.7			21.0			18.3			18.1			20.4			20.8		
Salinity (ppt)	2.7			0.7			15.4			21.9			0.0			0.0			0.9		
Turbidity (NTU)	5.6	5.5	Average 5.6	0.0	0.0	Average 0.0	7.7	7.7	Average 7.7	2.8	2.7	Average 2.8	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	4.9	4.8	Average 4.9
DO (mg/l)	9.74	9.72	Average 9.73	12.23	12.21	Average 12.22	10.14	10.13	Average 10.14	9.55	9.54	Average 9.55	11.34	11.36	Average 11.35	10.02	10.03	Average 10.03	10.85	10.83	Average 10.84
DO Saturation (%)	107	107	Average 107	130	130	Average 130	118	118	Average 118	102	102	Average 102	123	123	Average 123	111	111	Average 111	121	121	Average 121

Name
Prepared By: Jimmy Cheng

Signature


Date
26/3/2010

remark or
observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 27/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1050			1055			1105			1040			1115			1125			1135		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	8.27			8.26			7.54			7.93			8.38			7.63			7.13		
Temperature (oC)	20.2			18.9			19.1			19.3			18.5			19.7			20.6		
Salinity (ppt)	4.9			0.9			15.8			24.9			0.3			0.0			1.6		
Turbidity (NTU)	5.5	5.4	Average 5.5	0.0	0.0	Average 0.0	4.7	4.8	Average 4.8	7.1	6.9	Average 7.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	4.3	4.2	Average 4.3
DO (mg/l)	9.95	9.94	Average 9.95	11.75	11.73	Average 11.74	9.29	9.28	Average 9.29	9.43	9.41	Average 9.42	10.20	10.19	Average 10.20	9.64	9.64	Average 9.64	11.65	11.66	Average 11.66
DO Saturation (%)	113	113	Average 113	130	130	Average 130	101	101	Average 101	101	101	Average 101	108	108	Average 108	106	106	Average 106	130	130	Average 130

Name
Prepared By: Jimmy Cheng

Signature


Date
27/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 29/3/2010

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1220			1230			1240			1250			1210			1200			1145		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.1			<1			<1			<1		
pH value	6.98			7.61			7.26			7.77			7.63			7.93			7.55		
Temperature (oC)	19.8			19.0			19.3			19.4			19.2			20.0			19.2		
Salinity (ppt)	4.9			1.8			17.1			20.2			0.0			0.2			6.0		
Turbidity (NTU)	2.8	2.8	Average 2.8	0.0	0.0	Average 0.0	6.4	6.4	Average 6.4	7.6	7.6	Average 7.6	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	8.9	8.9	Average 8.9
DO (mg/l)	10.42	10.42	Average 10.42	12.35	12.35	Average 12.35	10.22	10.22	Average 10.22	10.42	10.42	Average 10.42	11.30	11.30	Average 11.30	9.73	9.73	Average 9.73	11.25	11.25	Average 11.25
DO Saturation (%)	119	119	Average 119	137	137	Average 137	111	111	Average 111	119	119	Average 119	119	119	Average 119	110	110	Average 110	124	124	Average 124

Name
Prepared By: Jimmy Cheng

Signature


Date
29/3/2010

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 31/3/2010 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1300			1310			1320			1250			1355			1345			1335		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	8.12			8.04			7.86			8.04			7.33			8.24			7.51		
Temperature (oC)	22.0			22.9			23.9			22.8			21.6			25.0			27.6		
Salinity (ppt)	6.9			8.2			21.3			20.9			0.0			0.4			8.7		
Turbidity (NTU)	0.0	0.0	Average	0.0	0.0	Average	11.2	11.2	Average	3.4	3.4	Average	1.4	1.4	Average	0.0	0.0	Average	14.3	14.3	Average
			0.0			0.0			11.2			3.4			1.4			0.0			14.3
DO (mg/l)	10.75	10.75	Average	13.25	13.25	Average	11.68	11.68	Average	9.97	9.97	Average	11.30	11.30	Average	11.86	11.86	Average	13.47	13.47	Average
			10.75			13.25			11.68			9.97			11.30			11.86			13.47
DO Saturation (%)	127	127	Average	158	158	Average	141	141	Average	120	120	Average	130	130	Average	147	147	Average	176	176	Average
			127			158			141			120			130			147			176

Name
Prepared By: Jimmy Cheng

Signature


Date
31/3/2010

remark or observation: _____

Appendix F2

Water Quality

Monitoring Lab report



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC100300134 Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 01-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 02-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	503	499	0.8	24.3
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID		C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time		01 Mar 2010 / 11:15		01 Mar 2010 / 11:30		01 Mar 2010 / 12:55			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	1.3	1.5	< 1.0	< 1.0	12.2	12.4		

TEST RESULTS	Sample ID		M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time		01 Mar 2010 / 12:35		01 Mar 2010 / 12:40		01 Mar 2010 / 12:45		01 Mar 2010 / 12:25	
	LOD	Units								
Suspended Solids (SS)	1	mg/L	11.6	11.9	2.1	2.3	12.4	12.1	11.2	10.9

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : Location M1 & WE3 and Location M3 & WE4 are the same location.

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300150

Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited

Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 03-03-2010

W.O. No.* : --

Sample Type* : River Water

Date Completed : 04-03-2010

GCE Serial No. : WQM032010

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	505	501	0.8	24.7
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	03 Mar 2010 / 14:40		03 Mar 2010 / 14:50		03 Mar 2010 / 15:00			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.4	1.5	13.9	14.0	13.0	12.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	03 Mar 2010 / 14:20		03 Mar 2010 / 14:25		03 Mar 2010 / 14:30		03 Mar 2010 / 14:10	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	19.8	20.2	2.8	2.9	150.8	152.8	47.2

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC100300168 Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 04-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 05-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	497	503	-1.2	25.2
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	--		--		04 Mar 2010 / 14:40			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	--	--	--	--	16.2	16.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	--		--		04 Mar 2010 / 14:30		04 Mar 2010 / 14:20	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	--	--	--	--	61.6	63.2	13.6 14.0

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300176

Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited

Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 05-03-2010

W.O. No.* : --

Sample Type* : River Water

Date Completed : 06-03-2010

GCE Serial No. : WQM032010

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results						
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L		
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	501	-0.6	24.3		
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29		
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	05 Mar 2010 / 15:00		05 Mar 2010 / 15:10		05 Mar 2010 / 15:25			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.3	1.1	< 1.0	< 1.0	20.8	21.2	
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	05 Mar 2010 / 15:50		05 Mar 2010 / 15:45		05 Mar 2010 / 15:40		05 Mar 2010 / 16:00	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	20.6	20.4	2.6	2.8	76.4	77.2	21.6

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300184 Date of Issue : 10-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 06-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 08-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	504	499	1.0	25.9
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time	06 Mar 2010 / 14:45			--		06 Mar 2010 / 14:55			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	--	--	18.2	17.8		

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	06 Mar 2010 / 15:20			--		06 Mar 2010 / 15:30		06 Mar 2010 / 15:15	
	LOD	Units								
Suspended Solids (SS)	1	mg/L	17.6	17.8	--	--	822.8	830.0	24.4	24.8

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300215 Date of Issue : 24-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 08-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 09-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results							
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L			
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	503	496	1.4	26.5			
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29			
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time	08 Mar 2010 / 15:50			--		08 Mar 2010 / 16:00			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	--	--	4.9	4.7		
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	08 Mar 2010 / 15:25			--		08 Mar 2010 / 15:35		08 Mar 2010 / 15:15	
	LOD	Units								
Suspended Solids (SS)	1	mg/L	11.0	11.2	--	--	11.5	11.6	8.0 7.9	

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC100300223 Date of Issue : 24-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 11-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 12-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	495	503	-1.6	24.7
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	11 Mar 2010 / 11:15		11 Mar 2010 / 11:25		11 Mar 2010 / 11:35			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	8.4	8.8	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	11 Mar 2010 / 10:55		11 Mar 2010 / 11:00		11 Mar 2010 / 11:05		11 Mar 2010 / 10:45		
	LOD	Units								
Suspended Solids (SS)	1	mg/L	6.5	6.8	2.8	2.9	31.6	31.4	11.2	11.3

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300231 Date of Issue : 24-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 12-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 13-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	502	497	1.0	24.9
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	12 Mar 2010 / 12:10		12 Mar 2010 / 12:20		12 Mar 2010 / 12:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	5.2	5.4	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	12 Mar 2010 / 11:45		12 Mar 2010 / 11:50		12 Mar 2010 / 12:00		12 Mar 2010 / 11:35		
	LOD	Units								
Suspended Solids (SS)	1	mg/L	4.6	4.4	1.1	1.2	12.5	12.5	5.2	5.0

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC100300249 Date of Issue : 24-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 13-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 15-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	496	502	-1.2	24.3
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	13 Mar 2010 / 12:10		13 Mar 2010 / 12:20		13 Mar 2010 / 12:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	7.8	7.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	13 Mar 2010 / 11:45		13 Mar 2010 / 11:50		13 Mar 2010 / 12:00		13 Mar 2010 / 11:40	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	2.8	3.0	1.3	1.1	8.6	8.7	8.4

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : K.L. FONG

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300257

Date of Issue : 25-03-2010

Client* : Environmental Pioneers & Solutions Limited

Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 15-03-2010

W.O. No.* : --

Sample Type* : River Water

Date Completed : 16-03-2010

GCE Serial No. : WQM032010

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results							
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L			
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	502	-0.8	25.1			
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29			
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time	15 Mar 2010 / 12:40		15 Mar 2010 / 12:50		15 Mar 2010 / 13:00				
	LOD	Units								
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	6.8	7.0		
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	15 Mar 2010 / 12:20		15 Mar 2010 / 12:25		15 Mar 2010 / 12:30		15 Mar 2010 / 12:10		
	LOD	Units								
Suspended Solids (SS)	1	mg/L	6.1	5.9	1.3	1.4	11.2	10.9	9.3	9.4

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300265 Date of Issue : 25-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 17-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 18-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	502	497	1.0	25.7
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	17 Mar 2010 / 14:10		17 Mar 2010 / 14:20		17 Mar 2010 / 14:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	5.9	6.1	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	17 Mar 2010 / 13:45		17 Mar 2010 / 13:50		17 Mar 2010 / 14:00		17 Mar 2010 / 13:40		
	LOD	Units								
Suspended Solids (SS)	1	mg/L	7.8	7.6	1.5	1.3	10.3	10.6	7.2	7.0


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300273 Date of Issue : 25-03-2010

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 19-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 20-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	502	505	-0.6	25.9
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	19 Mar 2010 / 14:50		19 Mar 2010 / 15:00		19 Mar 2010 / 15:10			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	17.6	18.0	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	19 Mar 2010 / 14:25		19 Mar 2010 / 14:35		19 Mar 2010 / 14:40		19 Mar 2010 / 14:15	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	16.8	17.0	1.6	1.4	14.0	14.8	11.2

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST SUMMARY ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300281

Date of Issue : 25-03-2010

Client* : Environmental Pioneers & Solutions Limited

Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 20-03-2010

W.O. No.* : --

Sample Type* : River Water

Date Completed : 22-03-2010

GCE Serial No. : WQM032010

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results						
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L		
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	502	-0.8	25.7		
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29		
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	20 Mar 2010 / 14:40		--		20 Mar 2010 / 14:50			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	--	--	7.5	7.9	
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	20 Mar 2010 / 14:25		--		20 Mar 2010 / 14:30		--	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	13.8	14.1	--	--	11.4	11.9	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300639 Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 22-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 23-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	491	493	-0.4	26.9
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	22 Mar 2010 / 15:30		22 Mar 2010 / 15:40		22 Mar 2010 / 15:50			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	13.9	13.3	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	22 Mar 2010 / 16:15		22 Mar 2010 / 16:10		22 Mar 2010 / 16:05		22 Mar 2010 / 16:25	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	117.6	114.8	2.6	2.5	12.1	12.4	13.4


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist

Checked By : GU CHIN



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300647 Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 23-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 25-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	490	485	1.0	23.3
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID		C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time		23 Mar 2010 / 16:10			--		--			
	LOD	Units									
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	--	--	--	--			

TEST RESULTS	Sample ID		M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time		23 Mar 2010 / 16:20			--		--		--	
	LOD	Units									
Suspended Solids (SS)	1	mg/L	29.2	30.0	--	--	--	--	--	--	


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300655

Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited

P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 24-03-2010

W.O. No.* : --

Sample Type* : River Water

Date Completed : 25-03-2010

GCE Serial No. : WQM032010

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results						
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L		
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	490	485	1.0	23.3		
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29		
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	24 Mar 2010 / 16:10		--		--			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.5	1.5	--	--	--	--	
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	24 Mar 2010 / 16:20		--		--		--	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	11.8	12.0	--	--	--	--	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300663 Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 26-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 27-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	488	490	-0.4	25.1
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	26 Mar 2010 / 11:10		26 Mar 2010 / 11:20		26 Mar 2010 / 11:00			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	< 1.0	< 1.0	< 1.0	7.9	8.0	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	26 Mar 2010 / 10:45		26 Mar 2010 / 10:50		26 Mar 2010 / 11:30		26 Mar 2010 / 10:35		
	LOD	Units								
Suspended Solids (SS)	1	mg/L	5.2	5.1	1.8	1.5	12.4	12.1	6.7	6.2

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300671 Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 29-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 30-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	507	497	2.0	23.1
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	27 Mar 2010 / 11:15		27 Mar 2010 / 11:25		27 Mar 2010 / 11:35			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	< 1.0	1.1	< 1.0	< 1.0	10.6	9.8	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	27 Mar 2010 / 10:50		27 Mar 2010 / 10:55		27 Mar 2010 / 11:05		27 Mar 2010 / 10:40	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	7.4	7.3	< 1.0	1.1	11.7	11.2	12.3


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300689 Date of Issue : 01-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 30-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 31-03-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	489	502	-2.6	24.5
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	29 Mar 2010 / 12:10		29 Mar 2010 / 12:00		29 Mar 2010 / 11:45			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.0	1.0	< 1.0	< 1.0	15.0	15.0	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	29 Mar 2010 / 12:20		29 Mar 2010 / 12:30		29 Mar 2010 / 12:40		29 Mar 2010 / 12:50	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.5	5.0	1.7	1.5	8.8	8.3	10.1

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : K.L. FONG

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC100300697 Date of Issue : 07-04-2009

Client* : Environmental Pioneers & Solutions Limited P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 31-03-2010

W.O. No.* : -- Sample Type* : River Water Date Completed : 01-04-2010

GCE Serial No. : WQM032010 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	504	499	1.0	25.9
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	31 Mar 2010 / 13:55		31 Mar 2010 / 13:45		31 Mar 2010 / 13:35			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.6	1.3	< 1.0	< 1.0	11.6	11.4	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	31 Mar 2010 / 13:00		31 Mar 2010 / 13:10		31 Mar 2010 / 13:20		31 Mar 2010 / 12:50	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.4	4.6	2.0	1.7	12.3	11.7	10.4


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : K.L. FONG

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist

Checked By : GU CHIN

Appendix G
Monitoring Schedule
for Feb 2010

Environmental Pioneers and Solutions Limited

DC/2006/11 - DRAINAGE IMPROVEMENT IN SOUTHERN LANTAU

Master Schedule of EM&A works in March 2010

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
2/28	3/1	3/2	3/3	3/4	3/5	3/6
	WQM, EWQM at: 12:52		WQM at: 14:07	additional WQM at: 14:30	WQM at: 15:30 Ecological Survey Noise monitoring	additional WQM at: 15:20
3/7	3/8	3/9	3/10	3/11	3/12	3/13
	additional WQM at: 15:25			WQM at: 10:54	WQM at: 11:24 Noise monitoring	WQM at: 11:48
3/14	3/15	3/16	3/17	3/18	3/19	3/20
	WQM at: 12:37	Ecological Survey	WQM at: 13:26		WQM at: 14:22 Noise monitoring	additional WQM at: 14:25
3/21	3/22	3/23	3/24	3/25	3/26	3/27
	WQM at: 16:18	additional WQM at: 16:20	additional WQM at: 16:20		WQM at: 10:00 Noise monitoring	WQM at: 10:45
3/28	3/29	3/30	3/31			
	WQM at: 11:57		WQM at: 13:09			

Noise Monitoring Locations: Total 4 Locations as N1, N2, N3 and N4


Water Quality Monitoring (WQM) Locations: Total 7 Locations as M1, M2, M3, M4, C1, C2 and C3

Ecological Water Quality Monitoring (EWQM) Locations: Total 6 Locations as WE1, WE2, WE3, WE4, WE5 and WE6


Appendix I

Graphical plot of water
quality monitoring
results (SS, DO,
turbidity)


Graphical Plot of Turbidity Trend M1&C1 (Dec 09 - Mar 10)

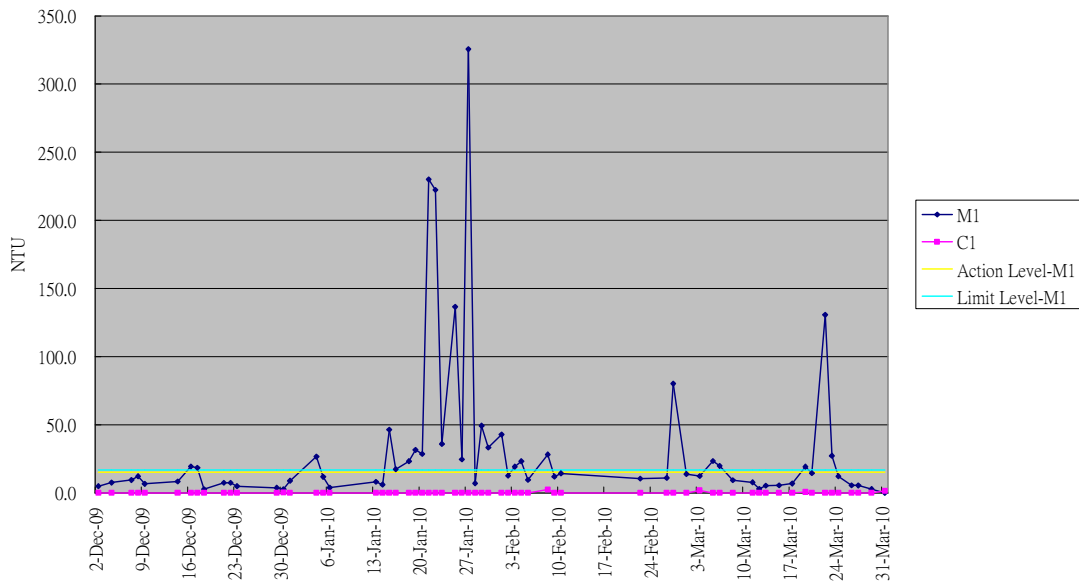


Graphical Plot of Turbidity Trend M2&C2 (Dec 09 - Mar 10)

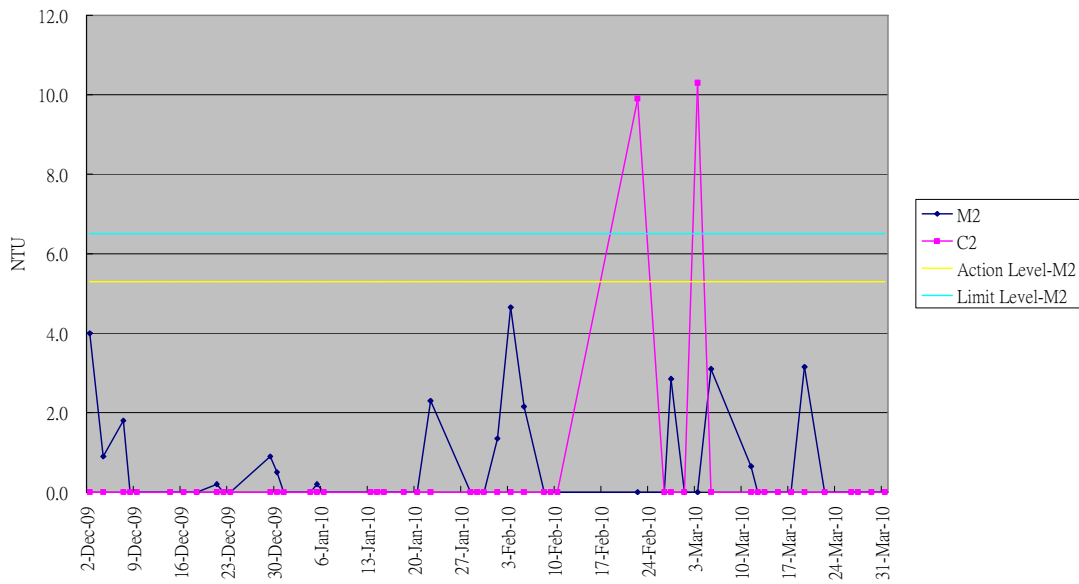


Graphical Plot of Turbidity Trend M3&C3 (Dec 09 - Mar 10)

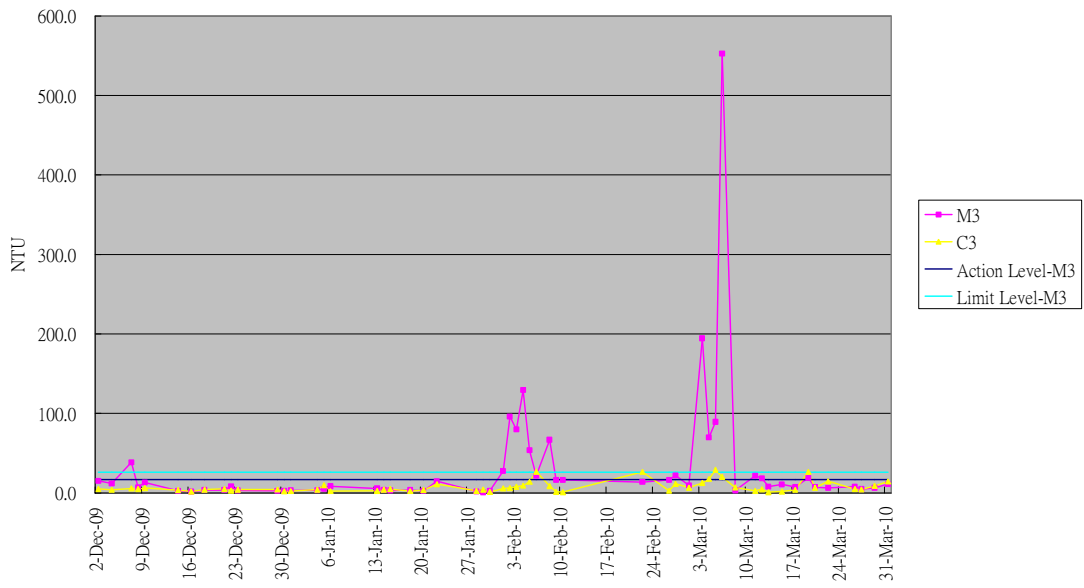


Graphical Plot of Turbidity Trend M4 (Dec 09 - Mar 10)

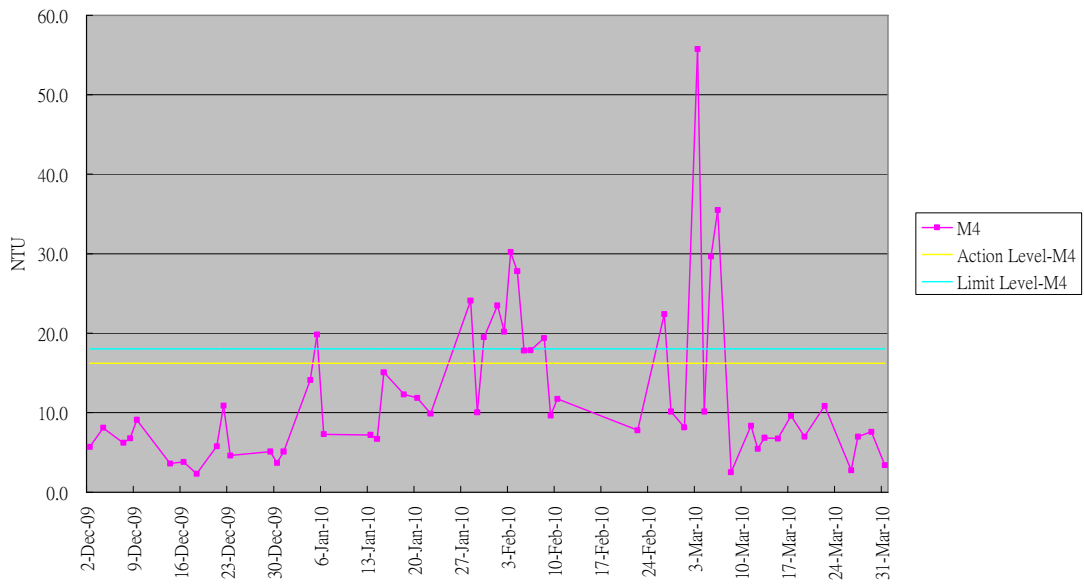


Graphical Plot of Dissolved Oxygen Trend M1&C1 (Dec 09 - Mar 10)

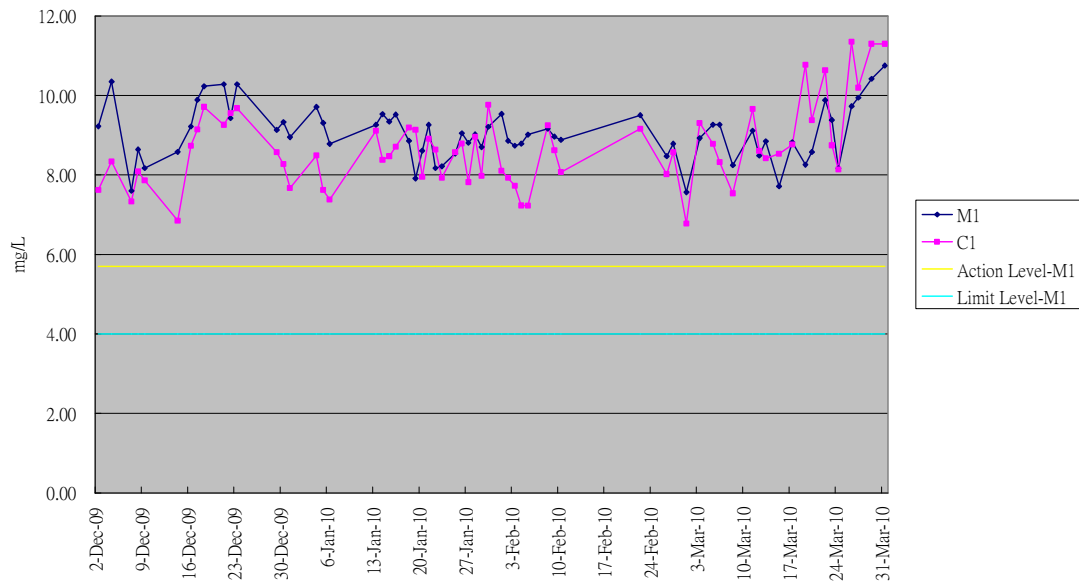


Graphical Plot of Dissolved Oxygen Trend M2&C2 (Dec 09 - Mar 10)

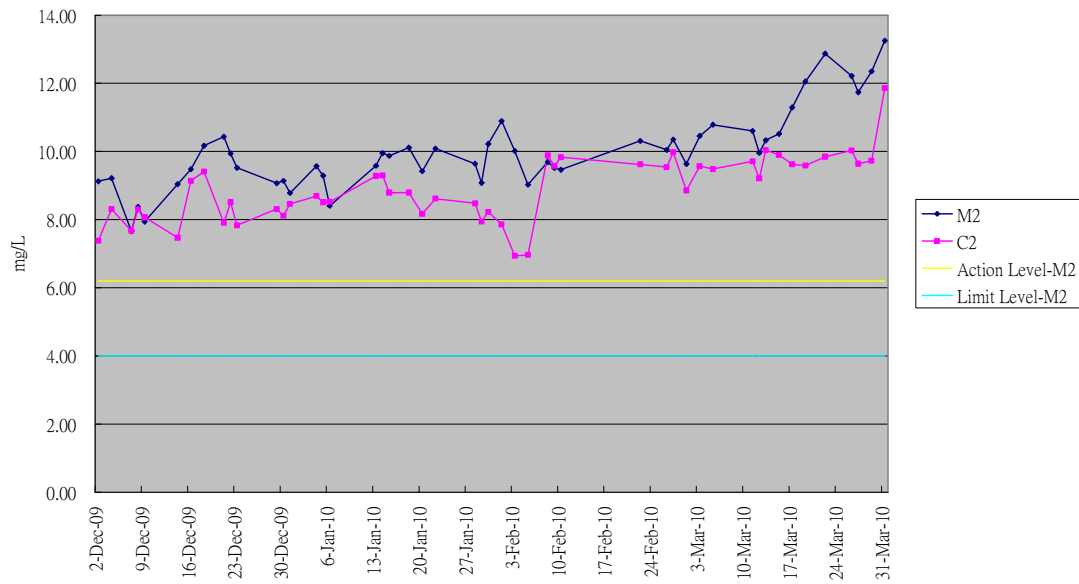


Graphical Plot of Dissolved Oxygen Trend M3&C3 (Dec 09 - Mar 10)

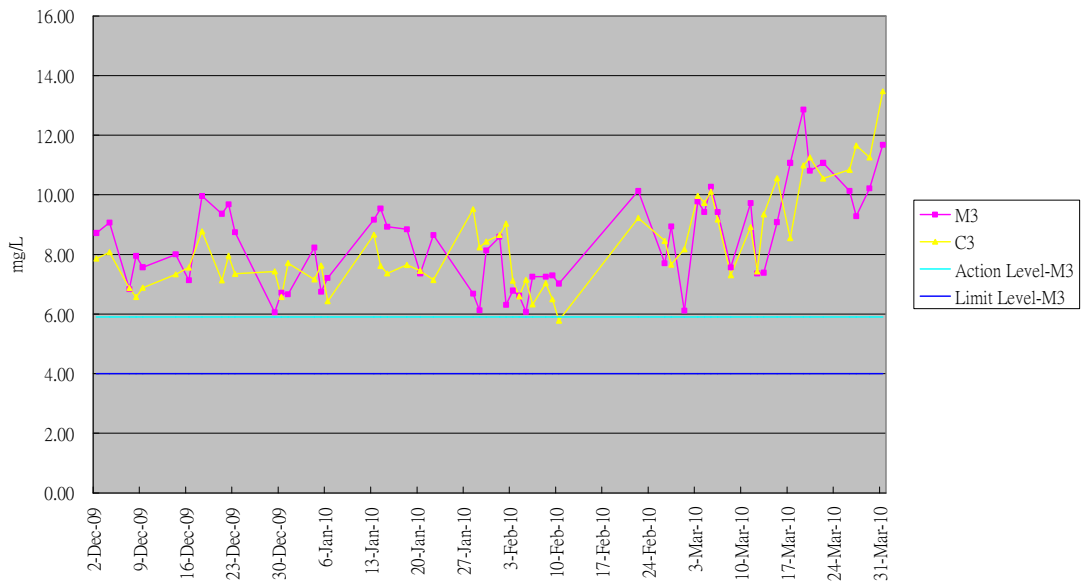


Graphical Plot of Dissolved Oxygen Trend M4 (Dec 09 - Mar 10)

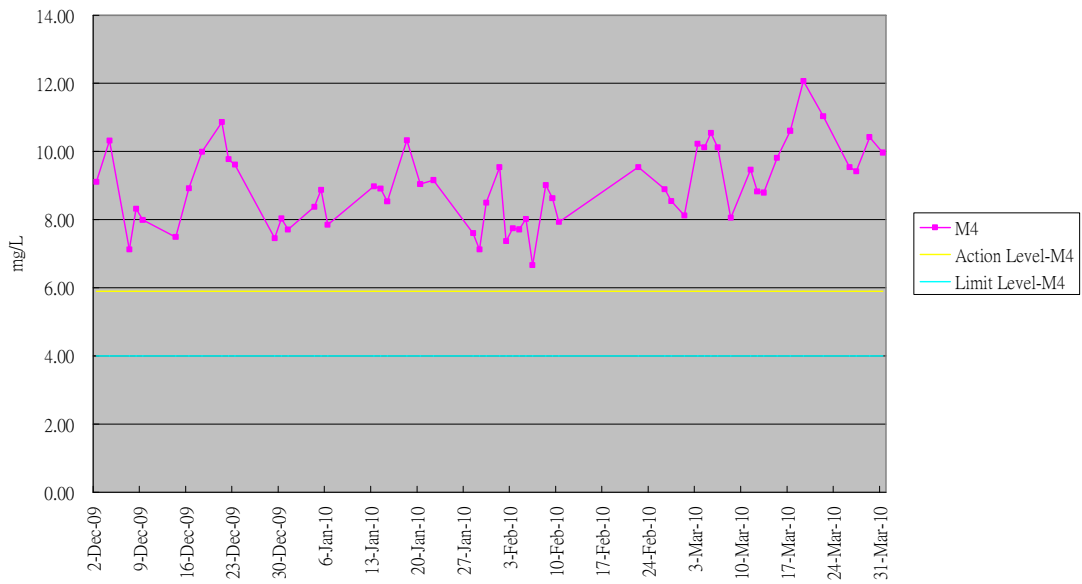


Graphical Plot of Suspended Solid M1&C1 (Dec 09 - Mar 10)

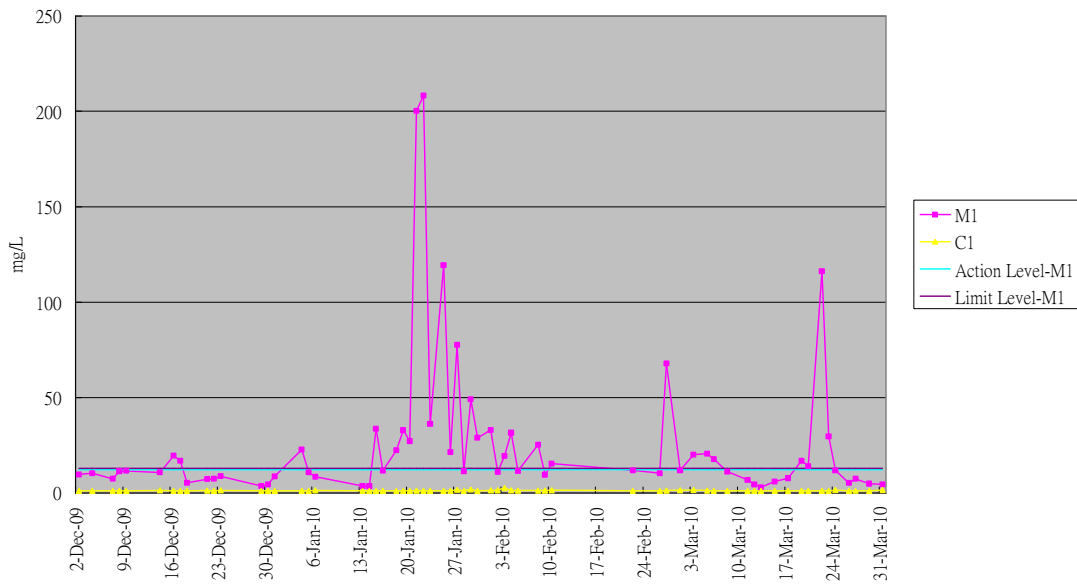


Graphical Plot of Suspended Solid M2&C2 (Dec 09 - Mar 10)

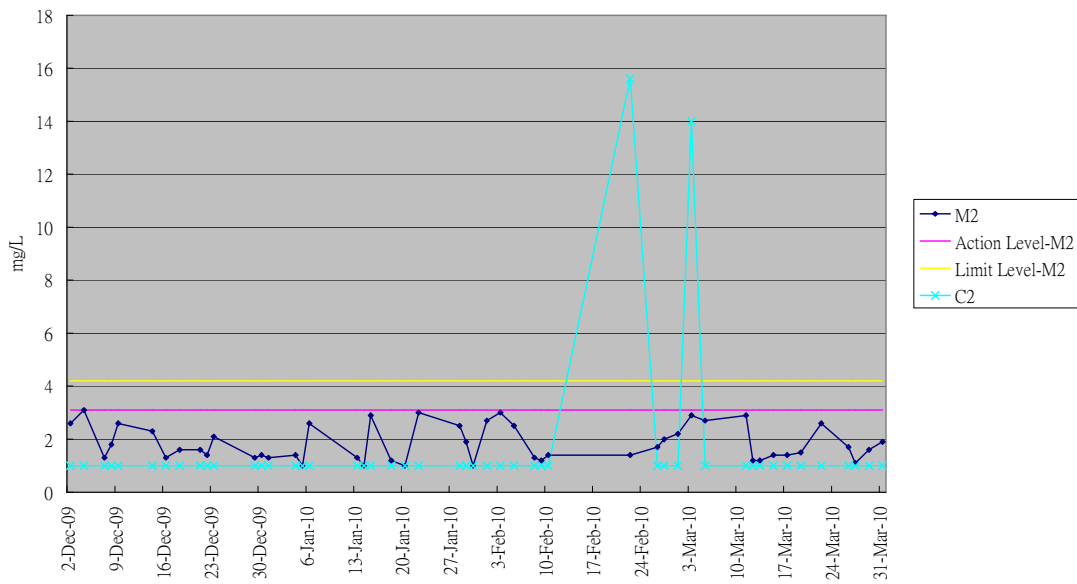

Graphical Plot of Suspended Soild M3&C3 (Dec 09 - Mar 10)


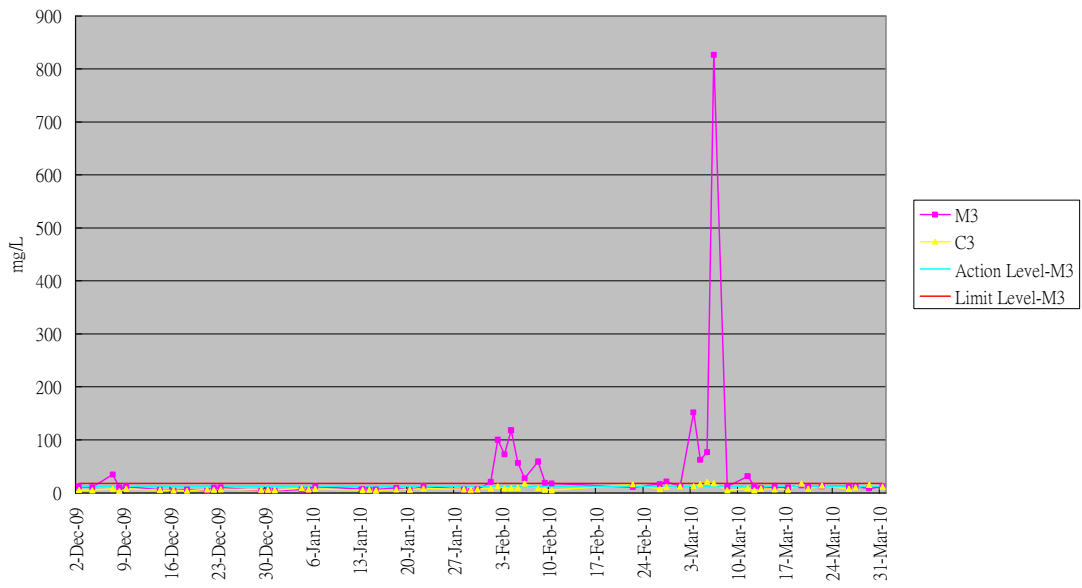


Graphical Plot of Suspended Soild M4 (Dec 09 - Mar 10)

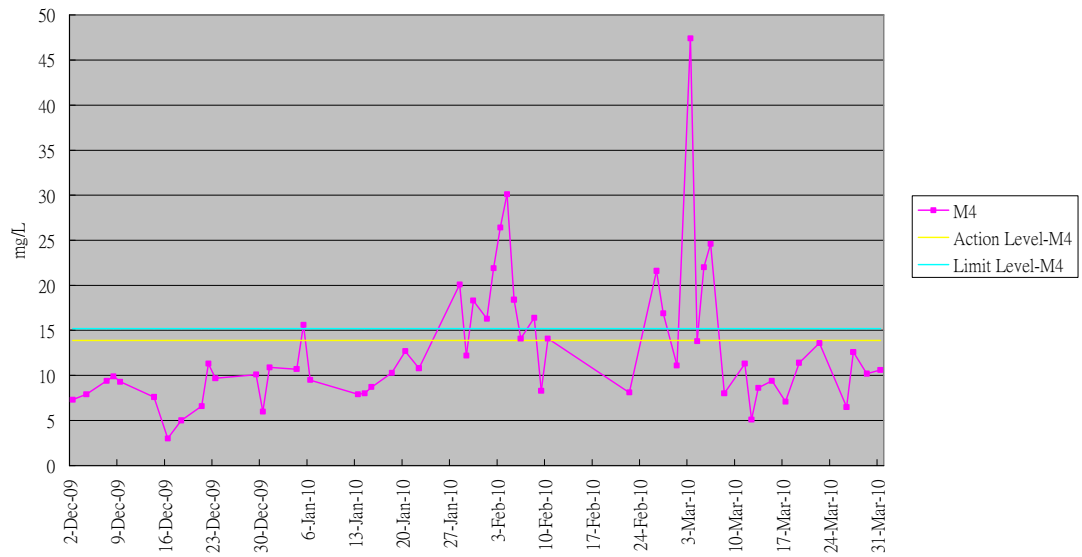


Appendix J

Graphical plot of noise
monitoring results

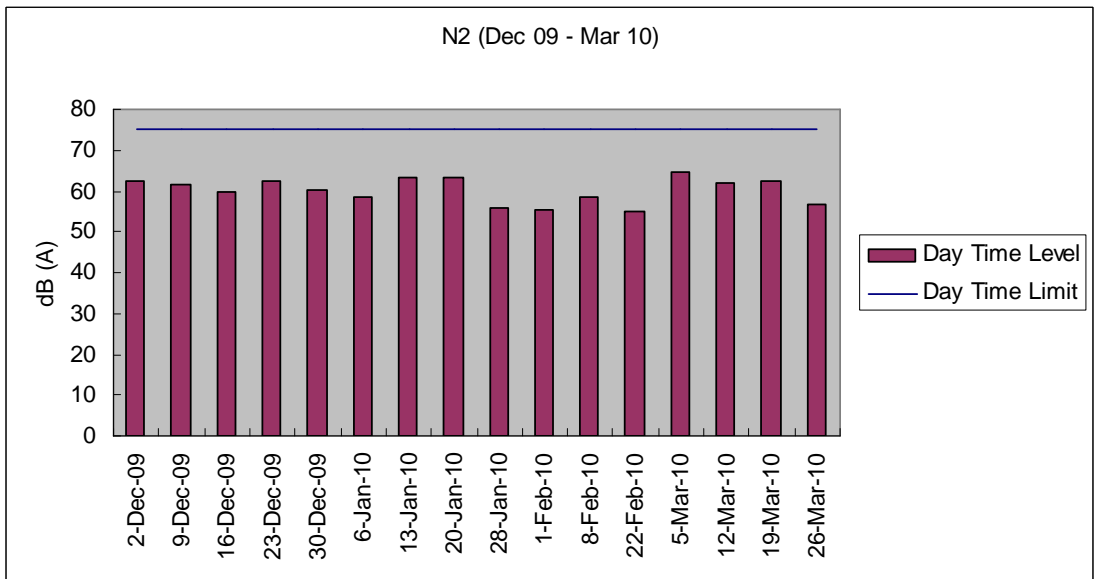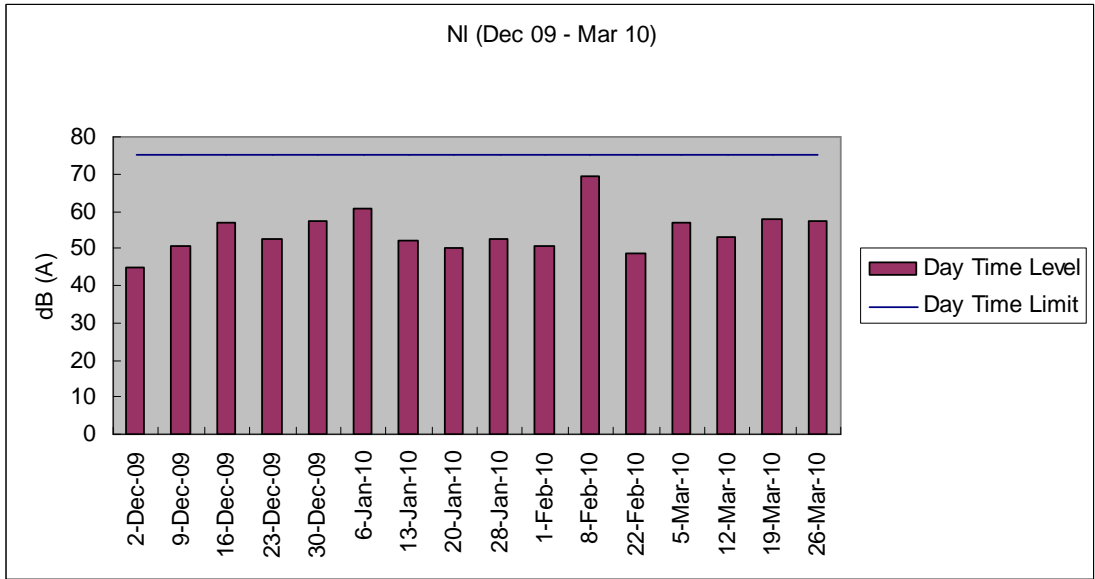

N3 (Dec 09 - Mar 10)

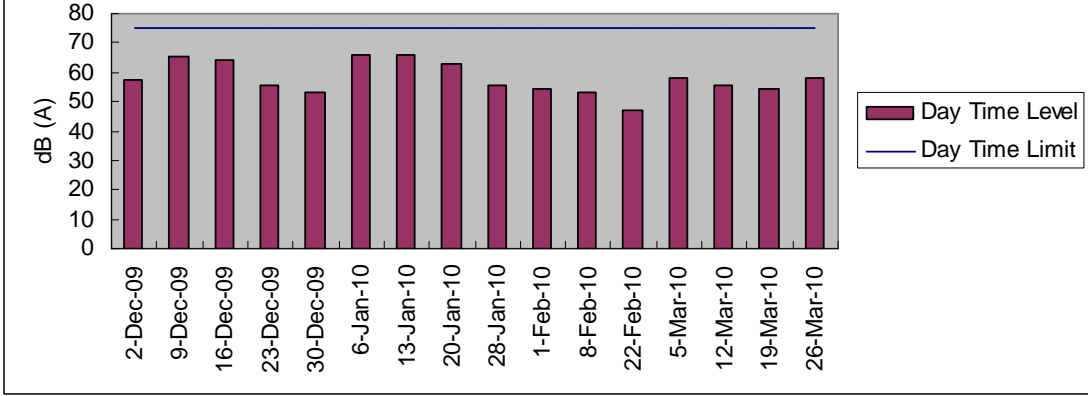

N4 (Dec 09 - Mar 10)

