

Drainage Service Department

Monthly Environmental Monitoring & Auditing report for

Contract No.DC/2006/11

Drainage Improvement in Southern Lantau

May 2011

Environmental Pioneers & Solutions Limited

Flat B, 6/F, Hop Shi Factory Building,


29 Lee Chung Street, Chai Wan, Hong Kong

Tel: 2556 9172

Fax: 2856 2010


APPROVAL SHEET

Prepared and Certified by: ET Leader (Environmental Pioneers & Solutions Limited)

Signature: 
Miss Patricia Chung
(ET* Leader)



Date: 22/7/2011

Signature: 
Mr. Vincent Lai
(Ecologist)

Date: 20/7/2011

* ET – Environmental Team

TABLE of CONTENT

TABLE of CONTENT	ii
EXECUTIVE SUMMARY	iv
1. Introduction	1
2. Project Information	1
2.1 Construction program	1
2.2 Project Organization	2
2.3 Key Personal Contact information chart	2
3. Construction Stage	3
3.1 Construction Activities in the reporting month	3
3.2 Construction Activities for the coming month	3
3.3 Environmental Status	3
4. Noise Monitoring	4
4.1 Monitoring Parameters and Methodology	4
4.2 Monitoring Equipment	4
4.3 Monitoring Locations	5
4.4 Monitoring Results and Interpretation	7
4.5 Action and Limit level for Construction noise	7
4.6 Noise Mitigation Measures	9
5. Water Monitoring	10
5.1 Water Quality Monitoring Parameters and methodology	10
5.2 Monitoring Equipment	10
5.3 Monitoring Locations	11
5.4 Monitoring Frequency	13
5.5 Monitoring Results and Interpretation	13
5.6 Action and limit level for Water Quality	15
5.7 Water Quality Mitigation Measures	17
5.8 Water Monitoring Schedule for the Next reporting period	17
6. Ecology Monitoring	18
6.1 Ecological Monitoring Parameters	18
6.2 Monitoring Equipment and Methodology	19
6.3 Monitoring Locations	20
6.4 Monitoring Frequency	23
6.5 Monitoring results	23
6.6 Action and Limit level for Monitoring of White-shouldered Starlings	31

6.7	Ecological monitoring Schedule	31
7.	Action taken in Event of Exceedence	32
8.	Construction waste disposal.....	33
9.	Status of Permits and Licenses obtained.....	34
10.	Complaint Log	35
11.	Site Environmental Audits	35
11.1	Site Inspection.....	35
11.2	Compliance with legal and Contractual requirement.....	37
11.3	Environmental Complaint and follow up actions.....	37
12.	Future key issues.....	37
13.	Conclusions.....	38

APPENDIXES

Appendix A	Construction Programme and location plan
Appendix B	Key Personal Contact information chart
Appendix C	Calibration Certificates for measuring instruments
Appendix D1	Plant species recorded at Pak Ngan Heung River (N)
Appendix D2	Plant species recorded at Pak Ngan Heung River (S)
Appendix D3	Plant species recorded at Luk Tei Tong River
Appendix D4	Ecological Water Monitoring results (on-site measurement)
Appendix D5	Ecological Water Monitoring results (lab-report)
Appendix E	Construction Noise Monitoring Data Sheet
Appendix F1	Water Quality Monitoring Data Sheet
Appendix F2	Water Quality Monitoring Lab report
Appendix G	Monitoring Schedule for May 2011
Appendix H	Implementation status of environmental protection / mitigation measures
Appendix I	Graphical plot of water quality monitoring results (SS, DO, turbidity)
Appendix J	Graphical plot of noise monitoring results

EXECUTIVE SUMMARY

This is the thirty-third monthly environmental Monitoring and audit (EM&A) report for “Drainage Improvement in Southern Lantau Investigation”. The environmental permit number is “EP-237/2005/B”. The report concludes the impact monitoring for the activities undertaken during the period of 1 May 2011 to 30 May 2011. Reconstruction of EVA on top of the PNH Box Culvert, landscaping works and railing installation were major site activities being carried out within this reporting month.

Noise, water quality and ecological monitoring were performed. Results obtained were checked against the previously established Action / Limit (A/L) levels. Additionally, the implementation status of environmental mitigation measures, event / action plan and environmental complaint handling procedures were inspected during weekly site environmental audit.

In general, waste management was satisfactory during the reporting month.

Impact monitoring for construction noise was conducted in the reporting period. No exceedance of A/L level was reported.

Refer to EPD memo received on 4 May 2011, post-construction water quality monitoring was started from 4 May 2011 to 1 June 2011. In this report, water quality results of 1 June 2011 were not included, which will be reported at the coming monthly report.

Furthermore, Total 23 non-compliance events of water quality criteria were recorded in this reporting period. For the non-compliance events, no particular observation of defective site activities were found causing water contamination and such conditions were believed to be mainly attributed by natural fluctuation.

During ecological monitoring survey, no White-shouldered Starling was recorded breeding in the watch tower. There was no sign of disturbance from the Project to the watch tower. The watch tower may not be suitable for birds as nesting habitat. In addition, no disturbance on the flora and fauna in the river channels were observed during the ecological monitoring.

There was no complaint, notification of any summons and successful prosecutions against the project received during the reporting period.

Future site activities to be carried out will be mainly Reconstruction of EVA on top of the PNH and Landscaping works. It is expected that environmental impact in different aspects will be resulted from the works. With reference to the EM&A manual and mitigation measure report, mitigation measures are proposed to be taken, if necessary.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement.

1. Introduction

This is the thirty-third monthly Environmental Monitoring and Audit (EM&A) Report for “Drainage Improvement in Southern Lantau Investigation” project (Environmental Permit No. EP-237/2005/B)

2. Project Information

2.1 Construction program

Majority of construction works of “Drainage Improvement in Southern Lantau Investigation” project were completed in May 2011. The project comprises the following:

- Completion of Landscaping Box Culvert Area, Footpaths, Road surface of Ngau Shui Street and VO reconstruction of EVA at Pak Ngan Heung River;
- Completion of Box A-Footpaths at LTT River
- Removal of surplus boulder in river bank at Tai Tei Tong (TTT) River

Appendix A shows the construction program and location plan of the project.

2.2 Project organization

The Main Contractor, Yick Hing Construction Company Limited, has commissioned Environmental Pioneers & Solutions Limited and Ecosystems Limited as the Environmental Team, which comprises the environmental team leader, the ecologists and the environmental technicians to undertake the environmental monitoring and audit work for this project.

The environmental management structure and is shown in Fig 2.2.1.

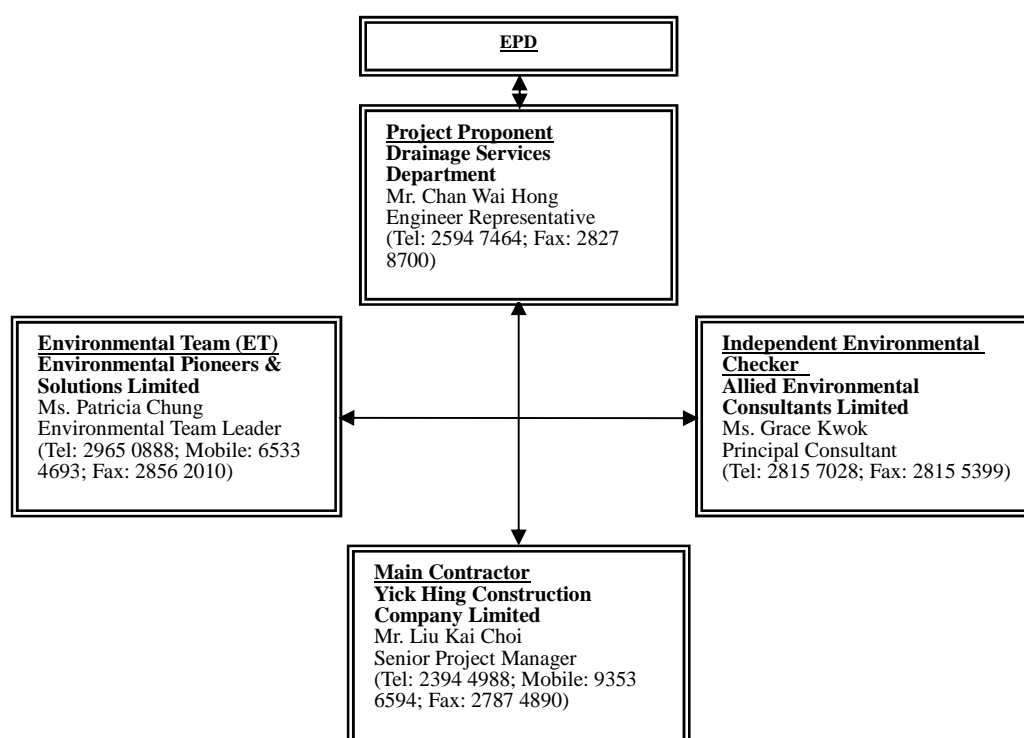


Figure. 2.2.1 Environmental Management structure for the project

2.3 Key personal contact information chart

Detailed contact of key persons involved in environmental aspect of the project is shown in Appendix B.

3. Construction Stage

3.1 Construction activities in the reporting month

Major activities in the reporting month included the followings:

1. Landscaping works.
2. Reconstruction of EVA on top of the PNH Box Culvert.
3. Installation of railing

3.2 Construction activities for the coming month

Proposed key construction works in the coming month will include:

1. Installation of railing installation..
2. Landscaping works.

3.3 Environmental Status

Appendix A shows the drawing of the project area.

Locations of the monitoring and control stations with environmental sensitive receivers are presented in Section 4.3, 5.3 and 6.3 for noise, water and ecological monitoring respectively.

4. Noise Monitoring

4.1 Monitoring Parameters and Methodology

The construction noise level was measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30minutes)}$ was used as the monitoring parameter for the impact monitoring in the time period between 0700 to 1900 hours on normal weekdays. For all other time period, $L_{eq(5minutes)}$ was employed for comparison with the Noise Control Ordinance (NCO) criteria.

Noise measurement results obtained from each monitoring location were recorded in the Construction Noise Monitoring Data Sheet (Appendix E) immediately after the measurement. As supplementary information for data auditing, statistical results L_{10} and L_{90} were also be recorded for reference.

In case of non-compliance with the construction noise criteria, more frequent monitoring, as specified in the Action plan in Table 4.5.2, shall be carried out. This additional monitoring shall be carried out until the recorded noise levels are rectified or proved to be irrelevant to the construction activities.

4.2 Monitoring Equipment

The sound level meters and calibrators comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum (TM) to the Noise Control Ordinance was deployed as monitoring equipment for noise measurement.

Noise measurement was not be made in the presence of fog, rain, wind with a steady speed exceeding $5ms^{-1}$ or wind with gust exceeding $10ms^{-1}$. Thus wind speed was checked by the portable wind speed indicator capable of measuring the wind speed in m/s. Table 4.2.1 summarizes the equipment list for noise monitoring

Table 4.2.1 Equipment List for Noise Monitoring

Equipment	Manufacturer & Model No.	Precision Grade	Qty
Integrated sound level meter	ACO Japan, model 6224	IEC 651 Type 1 IEC 804 Type 1	1
Windscreen	Microtech gefell model W2	N/A	1
Acoustical calibrator	Castle GA607	IEC 942 Type 1	1
Wind speed indicator	Kestrel K1000	N/A	1
Remarks: Calibration details for the sound level meter is given in Appendix C for reference			

4.3 Monitoring Locations

According to the Baseline Monitoring Report issued in May 2008 for the captioned project, four locations were alternative from the locations proposed in EM&A manual, were designated for baseline noise monitoring. For the data validation, impact noise monitoring was undertaken in the same locations during the construction phase of the project. The proposed monitoring locations are summarized in Table 4.3.1. Figure 4.3.1 shows the Noise Monitoring Locations

Noise measurement in each monitoring locations were taken at a point 1m from the exterior of the selected premises and at a height with no disturbance to the dweller and least obstructed view.

Table 4.3.1 Noise Monitoring Locations during Construction Phase

Identification No.	Noise Monitoring Locations
N1	No. 73, Village House, Ling Tsui Tau Tsuen (ground level)
N2	No. 31, Village House, Ling Tsui Tau Tsuen (ground level)
N3	Fence wall outside No. 5 village house adjacent to Luk Tei Tong River Outlet (ground level)
N4	No. 23, Village House, Tai Tei Tong River (ground level)

In accordance with the requirements in the EM&A manual, weekly impact monitoring was conducted. For the time period between 0700 and 1900 hours on normal weekdays, and noise parameter of $L_{eq(30minutes)}$ was measured. As if the construction works were carried out during restricted period (ie. 1900-2300, 2300-0700 of next day and Sundays / general holiday), impact monitoring that comprises 3 consecutive $L_{eq(5minutes)}$ would be carried out.

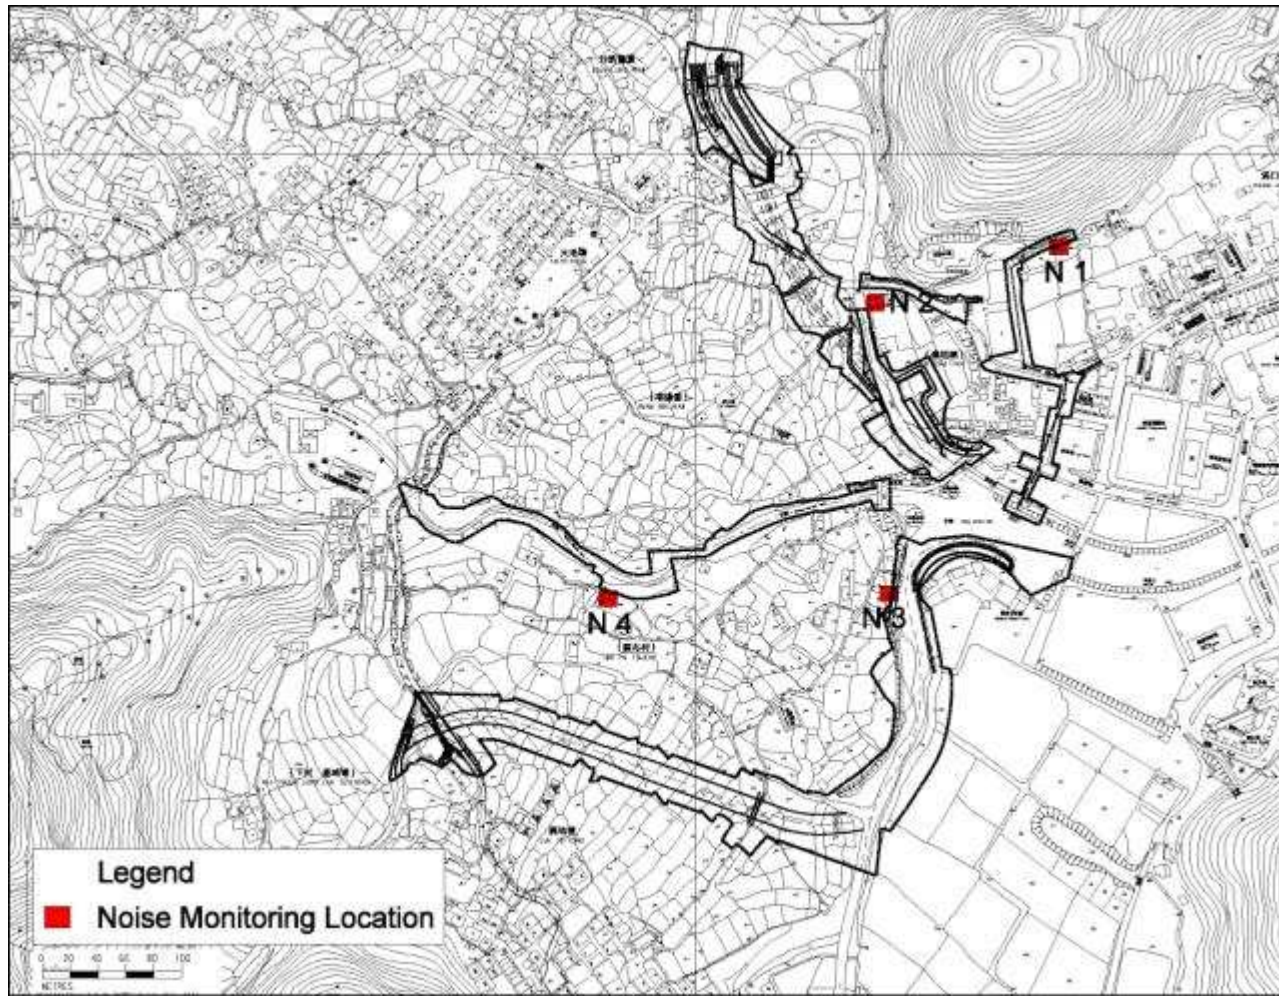


Figure 4.3.1 Impact noise monitoring locations

4.4 Monitoring Results and Interpretation

Relevant details of the noise monitoring results are presented in Table 4.4.1. The results, ranged between 46.5(A) and 67.8(A), were within the limit levels and therefore, no exceedance was found.

Table 4.4.1 Noise monitoring results

Table 4.4.1 Noise Monitoring Results for the reporting month							
Location	Parameter	Date	Time	L _{Aeq} dB(A)	Limit dB(A)	Exceedance	Weather
N1	Leq30min	6-May-11	13:25	55.9	75	N	Sunny
N1	Leq30min	13-May-11	14:45	54.9	75	N	Sunny
N1	Leq30min	20-May-11	12:10	67.8	75	N	Sunny
N1	Leq30min	27-May-11	12:45	55.1	75	N	Sunny
N2	Leq30min	6-May-11	12:50	47.5	75	N	Sunny
N2	Leq30min	13-May-11	14:10	47.6	75	N	Sunny
N2	Leq30min	20-May-11	12:45	54.1	75	N	Sunny
N2	Leq30min	27-May-11	12:10	54.8	75	N	Sunny
N3*	Leq30min	6-May-11	12:15	49.9	75	N	Sunny
N3*	Leq30min	13-May-11	13:35	57.3	75	N	Sunny
N3*	Leq30min	20-May-11	11:35	56.5	75	N	Sunny
N3*	Leq30min	27-May-11	11:35	54.2	75	N	Sunny
N4	Leq30min	6-May-11	11:40	48.7	75	N	Cloudy
N4	Leq30min	13-May-11	13:00	46.5	75	N	Cloudy
N4	Leq30min	20-May-11	10:55	48.8	75	N	Sunny
N4	Leq30min	27-May-11	11:00	47.7	75	N	Sunny

Remarks: Raw datasheet for noise monitoring are attached in Appendix E for reference.

Remark*: The equivalent noise level of N3 is corrected by +3 dB from the raw data result due to the fact that free field measurement was carried out in the location.

4.5 Action and Limit level for Construction noise

The Action and Limit (A/L) levels for construction noise are defined in Table 4.5.1. Should non-compliance of the criteria occur, action in accordance with the Action Plan in Table 4.5.2 should be carried out.

There was no exceedance recorded in the reporting month.

Time Period	Action Level	Limit Level
0700 – 1900 hours on normal weekdays	When one documented complaint is received	75dB(A)
Remarks: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.		

Table 4.5.2 Event / Action Plan for Construction Noise

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IC(E), ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IC(E); 2. Implement Noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E), ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

4.6 Noise Mitigation Measures

The following mitigation measures were observed from the weekly site inspection in the reporting month:

- Use of quiet powered mechanical equipment (PME)
- Implementation of the following good site practices:
 - Silencers or mufflers on construction equipment;
 - Mobile plant, if any, should be sited as far from noise sensitive receivers as possible; and
 - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.

5. Water Monitoring

5.1 Water Quality Monitoring Parameters and methodology

Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Turbidity, DO was measured in-situ while water samples were delivered to Accredited HOKLAS Laboratory for analysis of SS.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site were recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring location. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading would be discarded and further reading would be taken.

5.2 Monitoring Equipment

Turbidity, DO, Salinity, pH and temperature was measured by an instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

Detailed calibration records of the multimeter were shown in Appendix C for reference.

5.3 Monitoring Locations

Seven locations included a control station in upstream of each stream/ river, a monitoring station at the end of each stream/ river of the works area and a monitoring station at Silver River were proposed for the impact water quality monitoring. Water samples were collected at mid-depth of each proposed monitoring stations for measurements and sample collection. The Location Plan is shown in Figure 5.3.1 for reference.

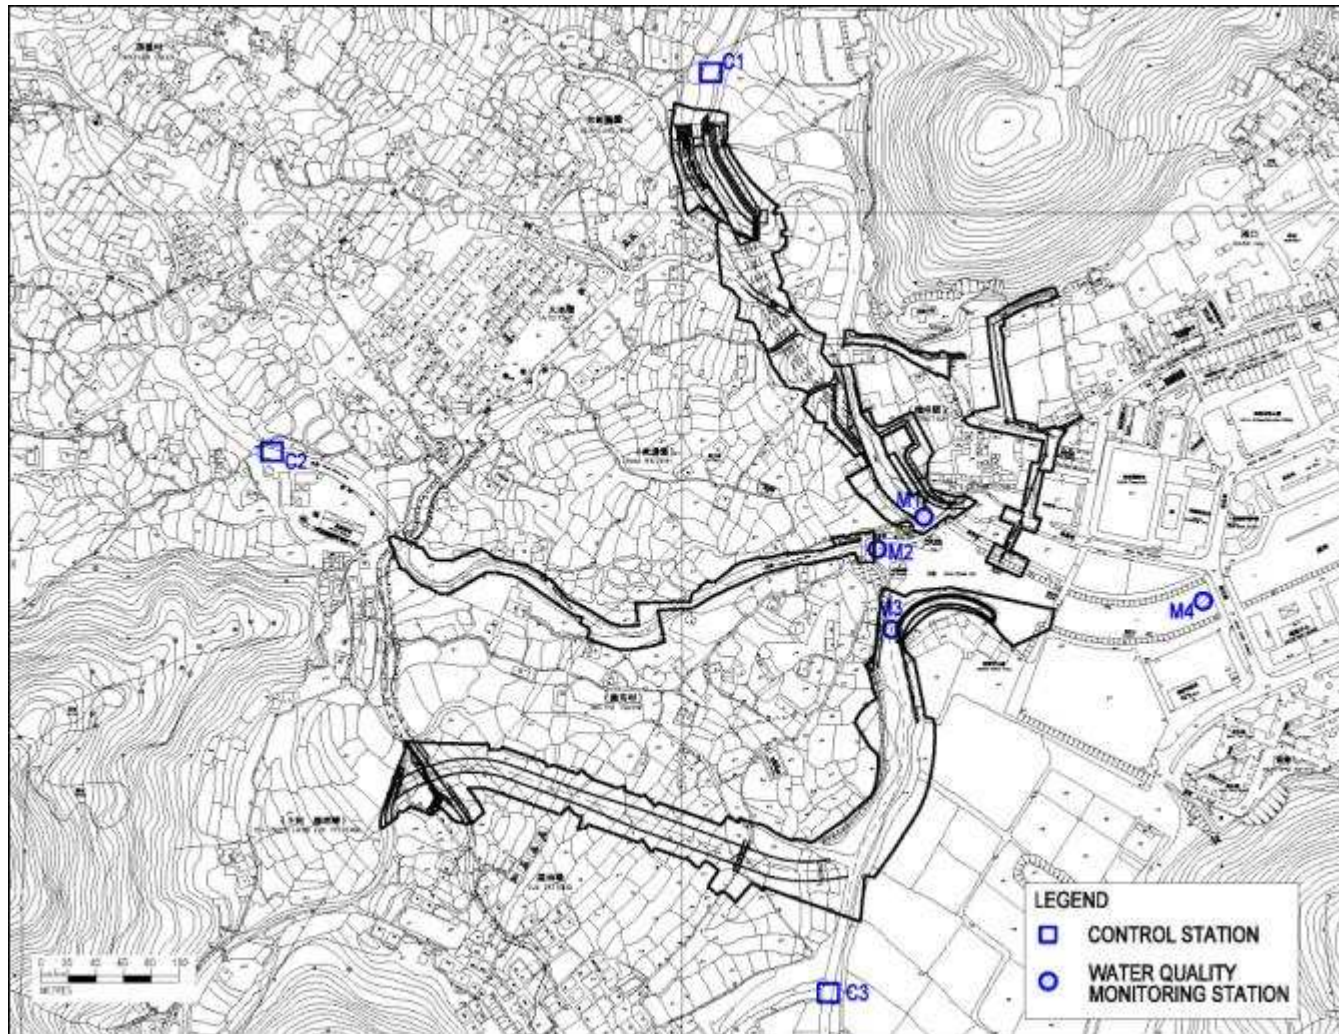


Figure 5.3.1 Water Quality Monitoring Locations

5.4 Monitoring Frequency

Impact water quality monitoring was undertaken three days per week and at ebb tides during the course of the construction river works. Upon the completion of the construction works, the monitoring exercises at the designated monitoring stations will be continued for four weeks in the same manner as the impact monitoring.

5.5 Monitoring Results and Interpretation

Water quality monitoring was carried out twelve times in this reporting month. Detailed on-site measurements and laboratory analysis reports including QA/QC results are shown in Appendix F1 and F2 respectively, while Table 5.5.1 presents consolidated results throughout the reporting month.

Total 23 non-compliance events of water quality limits (Turbidity and Suspended Solids) were recorded in this reporting month according to the established level. ET has arranged site investigations for the exceedance events.

For other non-compliance events, no particular observations of defective site activities were found causing the exceedance and such conditions were believed to be attributed by natural fluctuation.

Detailed information of the exceedance events and action taken were presented in Section 7.

Table 5.5.1 Water quality monitoring results in May 2011

	M1			M2			M3			M4		
	MIN	MAX	Average	MIN	MAX	Average	MIN	MAX	Average	MIN	MAX	Average
Turbidity (NTU)	0.0	7.5	2.2	0.0	2.8	1.0	0.0	9.7	4.0	0.0	7.7	2.7
DO (mg/l)	0.0	9.6	7.4	0.0	9.7	7.6	0.0	9.4	7.4	0.0	9.8	7.4
Suspended Solid (mg/l)	1.9	6.9	4.0	1.0	2.9	1.8	3.3	8.9	6.2	1.9	8.8	4.9

	C1			C2			C3		
	MIN	MAX	Average	MIN	MAX	Average	MIN	MAX	Average
Turbidity (NTU)	0.0	12.3	2.1	0.0	0.5	0.0	0.0	18.8	8.5
DO (mg/l)	7.3	9.3	8.5	7.1	9.6	8.8	6.0	9.3	7.4
Suspended Solid (mg/l)	1.3	13.8	4.1	1.0	3.3	1.6	4.4	16.4	10.0

* Remarks: Detection limit for Turbidity, DO and SS are 1 NTU, 0.1 mg/L and 1 mg/L respectively.

5.6 Action and limit level for Water Quality

Based on the criteria stipulated in EM&A manual Section 4.8 and baseline water quality monitoring data obtained, the A/L levels are shown in Table 5.6.1 and Table 5.6.2. If the water quality monitoring results at any impact stations exceeded the criteria, the actions in accordance with the Event and Action Plan in Table 5.6.3 should be taken.

Table 5.6.1 Water quality criteria for monitoring

Parameters	Action	Limit
DO in mg/L (mid-depth)	- 5%-ile of baseline data	- 4mg/L
SS in mg/L (mid-depth)	- 95%-ile of baseline data; or - 120% of control station's SS on the same day of measurement	- 99%-ile of baseline; or - 130% of control station's SS on the same day of measurement
Turbidity in NTU (mid-depth)	- 95%-ile of baseline data; or - 120% of control station's turbidity on the same day of measurement	- 99%-ile of baseline; or - 130% of control station's turbidity on the same day of measurement

Table 5.6.2 Action and Limit Levels established according to baseline data

Parameters	Monitoring locations							
	M1		M2		M3		M4	
	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level
Turbidity (NTU)	15.2	16.9	5.3	6.5	16.8	26.0	16.2	18.0
DO (mg/L)	5.7	4.0	6.2	4.0	5.9	4.0	5.9	4.0
SS (mg/L)	12.2	12.8	3.1	4.2	12.4	17.7	13.9	15.2

Remarks:

For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits

For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table 5.6.3 Event and action Plan for Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	Contractor
Action Level being exceed by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.
Action level being exceed by more than two consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; prepare to increase the monitoring frequency to daily 7. Repeat measurement on next day of exceedance 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER within three working days; 6. Implement the agreed mitigation measures.
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in <i>situ</i> measurement to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IC(E) and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IC(E) and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals in mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IC(E) on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; 6. Implement the agreed mitigation measures.

5.7 Water Quality Mitigation Measures

Construction Run-off and Drainage

The site practices outlined in ProPECC PN 1/94 ‘Construction Site Drainage’ should be followed as far as practicable during both construction and operation phase of the drainage improvement works in order to minimize surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge.

As recommended in the final EM&A manual, attention would be paid especially construction run-off and drainage, general construction activities, sewage discharged from construction workforce and river channel excavation works.

Contractor was recommended to provide sufficient water treatment facilities for accumulated site water and excavation activities carried out nearby river channel. Earth bunds should be provided to the construction site in / next to the river channel to form an enclosed, dry environment to minimize water quality impact.

5.8 Water Monitoring Schedule for the Next reporting period

Post-construction phase water quality monitoring has been completed on 1 June 2011. Therefore, no any water quality monitoring will be conduct in June.

As major construction activities, especially site cleaning works has been carried out by the end of May 2011. EDP has approved the post-construction phase water quality monitoring which was finished on 1 June 2011.

6. Ecology Monitoring

6.1 Ecological Monitoring Parameters

According to the Final EM&A Manual, a specific ecological monitoring programme of the improved section of PNH and LTT Rivers is recommended. The monitoring parameters required to measure in this project and survey methodology are described below:

- (1) Avifauna species and abundance: Birds will be surveyed quantitatively using transect count method. Birds within the river channel and on the riverbank will be identified and their abundance will be recorded.
- (2) Aquatic macroinvertebrate community species composition and abundance: Survey on aquatic fauna will focus on determination of the diversity and abundance of stream aquatic communities. Sampling methods, such as active searching, direct observation, netting, and kick sampling, will be determined according to the site conditions during field survey.
- (3) Fish community species composition and abundance: Sampling methods, such as active searching, direct observation, and hand netting, will be determined according to the site conditions during field survey.
- (4) Adult odonate community species composition and abundance: Adult dragonfly will be surveyed quantitatively using transect count method. Adult dragonflies within the river channel and on the riverbank will be identified and their abundance will be recorded. Species requiring close examination will be netted.
- (5) Aquatic, emergent and riparian vegetation community species composition and abundance: The area will be walked through. Plant species composition and their relative abundance will be recorded.
- (6) Surveys of White-shouldered Starling *Sturnus sinensis* will be conducted at the disused watchtowers next to LTT river. Breeding of the White-shouldered Starlings will be determined by checking signs of attempt to breed or sign of breeding which include carrying nesting materials, to-and-fro movement of adults carrying food, presence of recently fledged juveniles, etc. The number of breeding pairs and the site observation will be recorded whenever possible.

Water Quality Monitoring along LTT and PNH River as well as LTT bypass channel was carried out. Water quality monitoring will include Turbidity in Nephelometric Turbidity Unit (NTU), Dissolved Oxygen (DO) in mg/L and Suspended Solids (SS) in mg/L are required to measure in this project. Moreover, additional water monitoring parameters will be taken for the purposes of ecological monitoring of water quality in this project. The added information will include: BOD, Ammonia, Nitrate and Phosphate concentrations. Turbidity, DO, pH and water flow will be measured in-situ while water samples will be delivered to Accredited HOKLAS Laboratory accredited laboratory and the analyses followed the standard methods according to APHA Standard Methods for the Examination of Water and Wastewater, 20th Edition, or equivalent for analysis of SS, BOD, Ammonia, Nitrate and Phosphate concentrations.

Other relevant data such as monitoring location, time, water depth, temperature, salinity, weather conditions and any other special phenomena and work underway at the construction site will be recorded during sampling.

According to the requirement of the EM&A manual, two consecutive measurements for parameters of DO concentration, DO saturation and Turbidity are required to be taken at each monitoring. When the difference in value between the first and second reading of DO or Turbidity is more than 25%, the reading will be discarded and further reading will be taken.

6.2 Monitoring Equipment and Methodology

Turbidity, DO, Salinity, pH and Temperature will be measured by a instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

Suspended solid was determined by the water samples collected from the

monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection. Duplicate samples from each independent sampling event were undertaken during impact monitoring.

6.3 Monitoring Locations

According to the Final EM&A Manual, the improved section of the river channels will be divided into 50m long sections, and ecological survey will be carried out in each of the 50m sections. A total of nine sections will be divided for the two rivers which include:

- Two sections for existing upstream of PNH river (i.e. the proposed 80m long trapezoidal channel)
- Two sections for existing downstream of PNH river (i.e. the proposed 100m long rectangular channel)
- Five sections for existing Luk Tei Tong River (i.e. the proposed 240m long trapezoidal channel)

The disused watchtowers are located at the confluence of the three rivers and next to LTT river.

The Location Plan for ecological is shown in Figure 6.1 for reference.

The improved sections of the river channels require to carrying out water quality monitoring for the ecological purpose. The sampling points for impact monitoring was undertaken in the same place as the baseline monitoring proposed, where include:

- Three points for existing of PNH river
- Three points for existing of Luk Tei Tong River

The Location Plan for ecological water monitoring is shown in Figure 6.2 for reference.

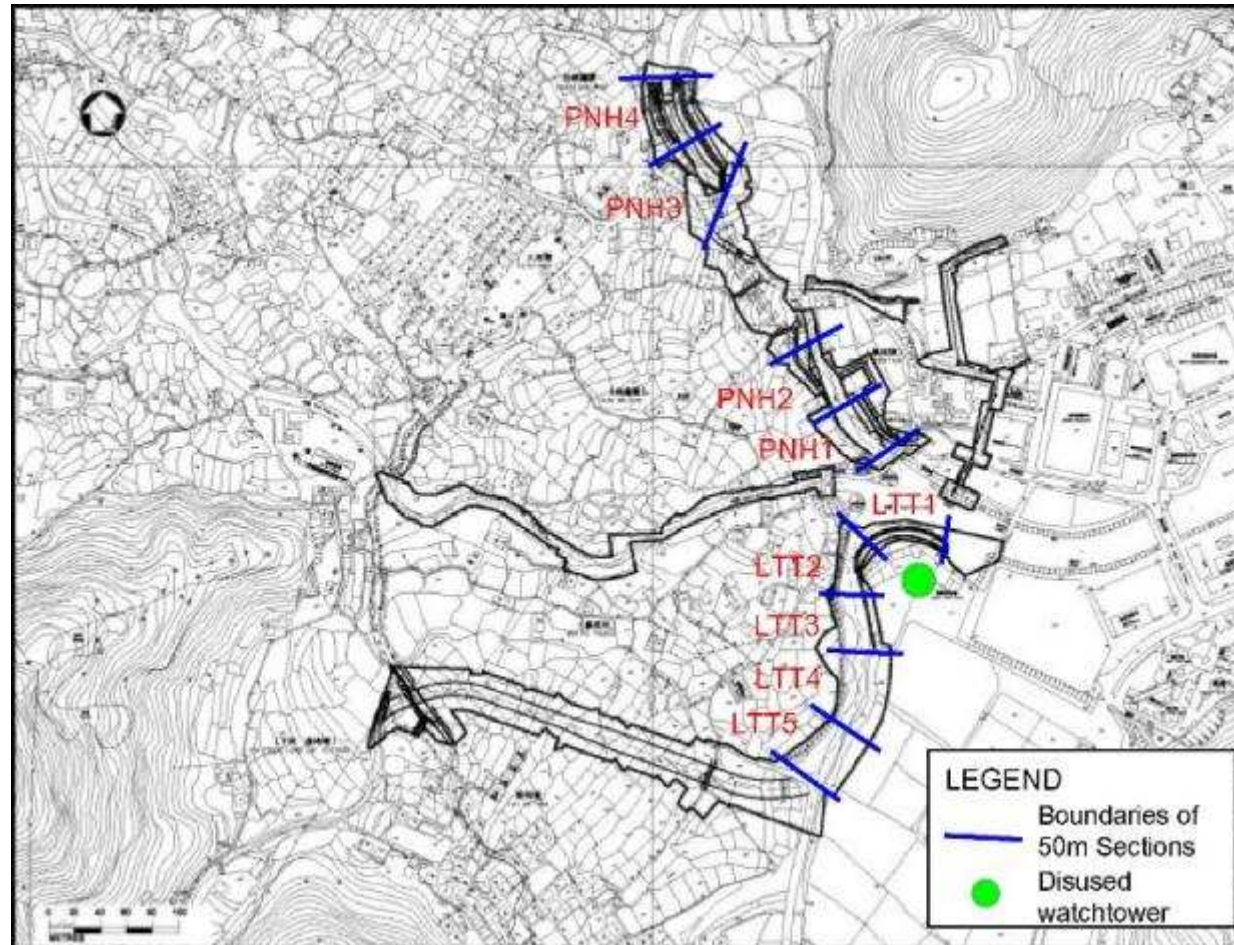


Figure 6.1 Ecological Monitoring Locations

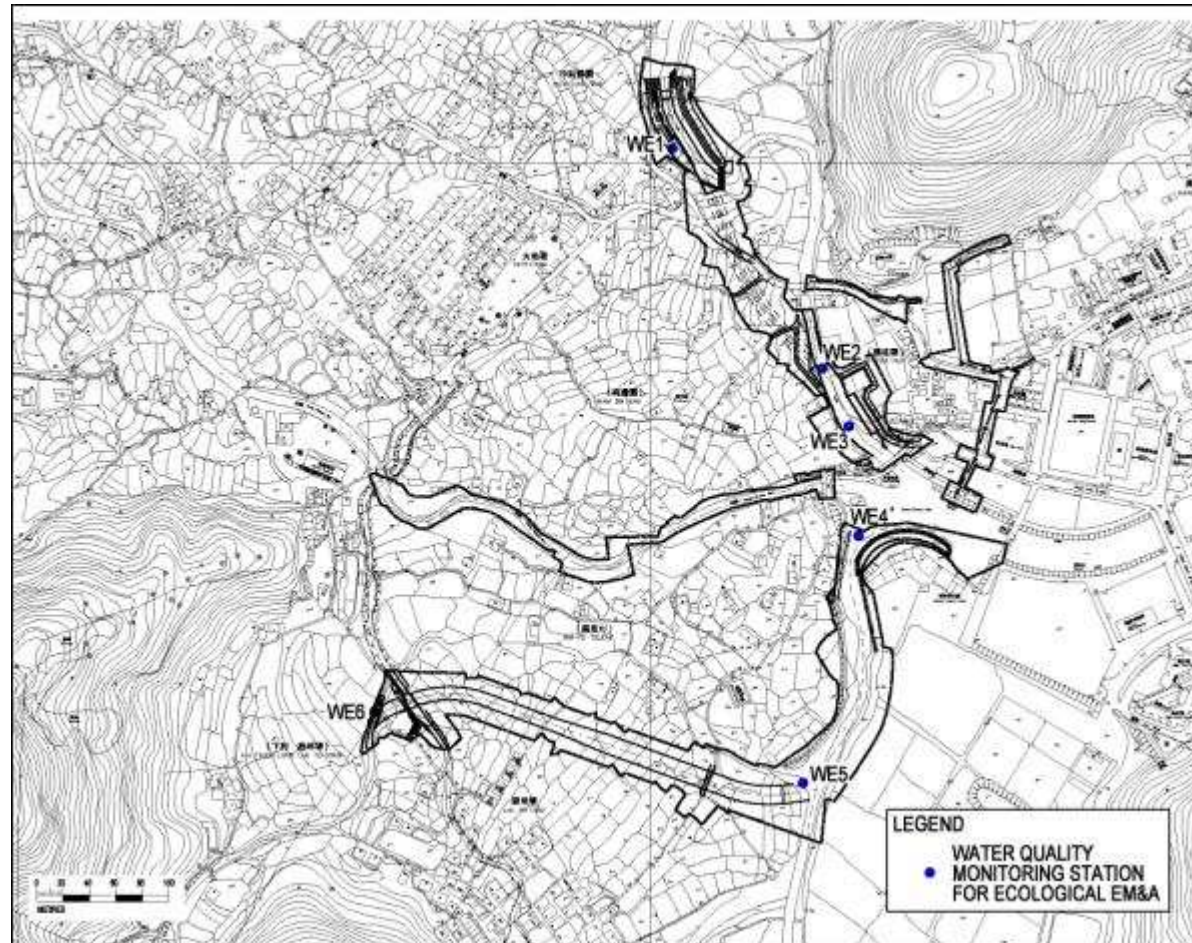


Figure 6.2 Ecological Water Quality monitoring locations

6.4 Monitoring Frequency

As proposed, ecological impact monitoring was carried out once for each monitoring location in the reporting month.

6.5 Monitoring results

Pak Ngan Heung Stream N and S sections

Vegetation

Surveys were conducted on 27 May 2011. During the current monitoring session, construction of new rock gabion wall was completed, and soft landscape works are underway. The understorey of the existing tree canopy along PNH4 was cleared and temporary works areas beyond both sides of gabions were planted with tree and shrub seedlings.

The walk through survey recorded a total of 52 species, including 16 trees, 2 shrub, 21 herb and 5 grass species (Appendix D1) on PNH N section. 39 of the species recorded are natives, while 13 were exotics. Remnants of vegetation including native trees (e.g. *Macaranga tanarius*) and grasses species (e.g. *Microstegium ciliatum*) were still seen along the east stream bank. A number of ruderal species colonised the sandy substrate occasionally deposited among stream bed rocks and gabions. These include *Mikania micrantha*, *Bidens pilosa* and *Emilia sonchifolia*. No species of conservation interest was recorded. No quantitative surveys were carried out on both PNH3 and PNH4 due to vegetation clearance and construction works on stream banks as part of the site clearance works under the project.

Vegetation was only found on remnants of the old concrete bank along PNH S section. A total of 5 species recorded, 3 of which were native and 2 were exotic. It was composed of isolated individuals of mangrove (*Kandelia obovata*), exotic shrub (*Lantana camara*) and native trees (*Ficus supbera*) (Appendix D2). No species of conservation interest was recorded.

Terrestrial Fauna

Surveys were conducted on 27 April 2011.

Two species of birds were recorded in the proposed work area of the Pak Ngan Heung River (Table 6.5.2). Both are common in Hong Kong.

Table 6.5.2 Avifauna in Pak Ngan Heung

Common names	Latin names	PNH 1	PNH 2	PNH 3	PNH 4	Commonness & distribution
Chinese Bulbul	<i>Pycnonotus sinensis</i>			1		CW
Red-whiskered Bulbul	<i>Pycnonotus jocosus</i>			1		CW
Magpie Robin	<i>Copsychus saularis</i>			1		CW
Japanese White-eye	<i>Zosterops japonica</i>				4	CW

CW = common and widespread

Three species of dragonfly were recorded in the proposed work area of the Pak Ngan Heung River (Table 6.5.3) in May 2011. All are very common in Hong Kong (Wilson 2004).

Table 6.5.3 Dragonfly in Pak Ngan Heung River

Common names	Latin names	PNH 1	PNH 2	PNH 3	PNH 4	Commonness & distribution
Green Skimmer	<i>Orthetrum sabina</i>			1		C
Crimson Dropwing	<i>Trithemis aurora</i>	1	1			A
Indigo Dropwing	<i>Trithemis festiva</i>	1				A

A = abundant

Aquatic fauna and fish

The construction works for the fish ladder inside PNH3 have been finished, and the flow in this section was restored. 7 species of fish and 3 crustacean

were recorded in the 4 sections at PNH. All are common and widespread in Hong Kong. Though Predaceous Chub was observed, the another one fish species of conservation concern reported in the EIA report, i.e. Flagtail *Kuhlia marginata*, was not recorded in PNH during the present monthly monitoring survey.

Table 6.5.4 Aquatic Invertebrates and fish in Pak Ngan Heung

Common names	Scientific names	PNH 1	PNH 2	PNH3	PNH4
Invertebrates					
Atyid shrimp	<i>Caridina elongata</i>				++
Palaemonid shrimp	<i>Macrobrachium hainanensis</i>			+	+
Crab	<i>Varuna litterata</i>				+
Mitten Crab	<i>Eriocheir japonica</i>				
Fish					
Mosquito fish	<i>Gamusia affinis</i>				++
Goby	<i>Rhinogobius duospilus</i>				++
Barcheek Goby	<i>Rhinogobius giurinus</i>				
Swordtail	<i>Xiphophorus hellerii</i>				
Six-banded Barb	<i>Puntius semifasciolatus</i>				
Unidentified Cichlid fish					+
Tilapia		+++	+++		
Predaceous Chub	<i>Parazacco spilurus</i>			+++	
Jarbua Terapon	<i>Terapon jarbua</i>	++	+		
Common Silver-biddy	<i>Gerres oyena</i>				
Mullet	<i>Mugil cephalus</i>	++	+++		
Broken-band Hillstream Loach	<i>Liniparhomaloptera disparis</i>				

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Luk Tei Tong Stream Section

Vegetation

Surveys were conducted on 27 May 2011. During the current survey, construction of concrete channel bank and rock gabions are completed, and soft landscape works are underway. Some remnants of vegetation and mangroves remained at both LLT1 and LLT2 respectively, while a few grass, herb and climber colonised the gabion of LLT3 and LLT4. A portion of the sediments and associated weedy vegetation between the mangrove at LLT2 and the gabion was gone, probably washed away by recent rainstorm. The mangrove stands remained intact.

The walk through survey recorded a total of 17 species, including 8 tree, 2 herb and 4 grass species (Appendix D3). 10 species recorded are natives, while 7 were exotics. No quantitative survey was carried out due to sporadic occurrence of colonised vegetation on the new gabion banks.

Terrestrial Fauna

The proposed work area of Luk Tei Tong River was divided into 5 sections. All recorded avifauna and dragonfly species are common in Hong Kong

Surveys were conducted on 26 May 2011.

A total of seven species of birds were recorded in these sections (Table 6.5.6). All are common in Hong Kong.

Table 6.5.6 Avifauna in Luk Tei Tong River

Common names	Latin names	LTT 1	LTT 2	LTT 3	LTT 4	LTT 5	Commonness & distribution
Little Egret	<i>Egretta garzetta</i>	12	1				CW
Great Egret	<i>Casmerodius albus</i>	1					CL
Black-crowned Night Heron	<i>Nycticorax nycticorax</i>		6				CL
Chinese Bulbul	<i>Pycnonotus sinensis</i>				3		CW

Red-whiskered Bulbul	<i>Pycnonotus jocosus</i>					2		CW
Magpie Robin	<i>Copsychus saularis</i>						1	CW
Crested Myna	<i>Acridotheres cristatellus</i>						5	CW

CW = common and widespread, CL = common/uncommon and localised

Five species of dragonfly were recorded in the Luk Tei Tong Riber in May 2011 (Table 6.5.7). All are common/very common in Hong Kong (Wilson 2004)

Table 6.5.7 Dragonfly in Luk Tei Tong River

Common names	Latin names	LTT 1	LTT 2	LTT 3	LTT 4	LTT 5	Commonness & distribution
Green Skimmer	<i>Orthetrum sabina</i>	1					C
Wandering Glider	<i>Pantala flavescens</i>	12			5		A
Variiegated Flutterer	<i>Rhyothemis variegata</i>	3				6	C
Crimson Dropwing	<i>Trithemis aurora</i>		1				A
Indigo Dropwing	<i>Trithemis festiva</i>					1	A

A = abundant, C = common

Aquatic invertebrates and fish

4 species of fish, 1 species of crustacean and 4 species of mollusks were recorded in the 5 sections at LTT. All are common and widespread in Hong Kong. The two fish species of conservation concern reported in the EIA report, i.e. Flagtail *Kuhlia marginata* and Predaceous Chub *Parazacco spilurus* were not recorded in LTT during the present monitoring as well as the baseline monitoring survey.

Table 6.5.8 Aquatic invertebrates and fish in Luk Tei Tong River

Common names	Scientific names	LTT1	LTT2	LTT3	LTT4	LTT5
Invertebrates						
Mangrove clam	<i>Geloina erosa</i>					
Rock oyster	<i>Saccostrea cuculata</i>	+++	+++			

Snail	<i>Melanoides tuberculata</i>				+++	++
Snail	<i>Terebralia</i> sp.					
Snail	<i>Nerita</i> sp.	+++	+++	+	+	
Snail	<i>Littoraria articulata</i>		+	+		
Crab	<i>Varuna litterata</i>					
Fiddler crab	<i>Uca lactea</i>					
Fiddler crab	<i>Uca arcuata</i>					
Fiddler crab	<i>Uca crassipes</i>					
Crab	<i>Perisesarma bidens</i>					
Mangrove mud crab	<i>Scylla paramamosain</i>					
Mitten crab	<i>Eriocheir japonica</i>					
Crab	<i>Varuna litterata</i>		+			
Fish						
Common mudskipper	<i>Periophthalmus cantonensis</i>	+	+			
Tilapia		+++	++			
Jarboa terapon	<i>Terapon jarbua</i>	+	+			
Mullet	<i>Mugil cephalus</i>	+++	+++	++		
Common Silver-biddy	<i>Gerres oyena</i>					
Barcheek Goby	<i>Rhinogobius giurinus</i>					

+ = Occasional, less than 5 individuals were found; ++ = Common, 5 – 20 individuals were found; +++ = Abundant, more than 20 individuals were found.

Disused Watchtowers

Surveys were conducted on 26 May 2011.

There was no sign (e.g., adults carrying food or nesting materials) of use of the watchtower as nesting habitat by White-shouldered Starling.

White-shouldered Starling was not observed during the May 2011 monitoring. No bird of other species was observed entering the watchtower.

Since the monitoring surveys commenced in August 2008, no bird was observed entering the watchtower. It seems the birds do not prefer the

watchtower as nesting habitat.

Ecological Water Quality Monitoring (EWQM)

EWQM was conducted on 27 May 2011. Monitoring results are summarized in table 6.9. Detailed on-site measurements and laboratory report are presented in appendix D4 and D5.

Table 6.10 shows the baseline results of Ecological Water Quality Monitoring, from the information given in Baseline Monitoring Report.

To review the results in table 6.9 in general, data obtained in the monitoring stations were similar to the results from the previous month.

Table 6.9 Summarized Ecological water quality monitoring results (27 May 2011)

Parameters	Limit of detection	WE1	WE2	WE3	WE4	WE5	WE6
Suspended Solid (mg/l)	1	2.95	3.45	3.55	4.85	7.2	4.05
Nitrogen (Ammonia) (mg/l)	0.01	0.09	0.16	0.68	0.25	1.79	0.08
Nitrogen (Nitrate) (mg/l)	0.01	0.20	0.35	0.52	1.39	0.35	0.11
Phosphorous (mg/l)	0.01	0.06	0.09	0.12	0.19	0.20	0.09
BOD ₅ (mg/l)	1	1.0	1.0	2.0	1.0	2.0	1.0
DO (mg/l)	0.01	7.25	7.97	7.98	6.04	6.83	10.7
Turbidity (NTU)	0.01	0.0	0.0	0.0	0.8	2.8	0.4
Temperature (oC)	0.1	25.4	26.5	25.3	29.3	29.3	28.3
pH	0.01	6.1	7.1	7.3	6.5	6.7	7.7
Salinity (ppt)	0.1	0	0	0.6	13.9	3.8	0.1
Conductivity (s/m)	0.1	7.9	14.6	0.1	2.1	0.7	20.6
Water Flow (m/s)	N/A	0.1	<0.1	0.1	0.1	0.1	<0.1

Table 6.10 Baseline Results of Ecological water quality monitoring

Parameters	WE1	WE2	WE3	WE4	WE5	WE6
Suspended Solid (mg/l)	1.0	2.0	3.0	3.0	<1	<1
Nitrogen (Ammonia) (mg/l)	0.07	0.12	0.11	0.23	0.03	0.02
Nitrogen (Nitrate) (mg/l)	0.12	0.13	0.13	0.31	0.04	0.05
Phosphorous (mg/l)	0.04	0.06	0.06	0.09	0.06	0.05
BOD ₅ (mg/l)	<2	<2	<2	<2	<2	<2
DO (mg/l)	6.58	6.82	6.37	7.61	6.87	5.70
Turbidity (NTU)	4.44	5.12	5.93	6.96	4.65	2.73
PH	6.4	7.1	7.0	6.8	6.6	6.1
Salinity (ppt)	<0.1	0.1	0.3	7.6	0.1	<0.1

6.6 Action and Limit level for Monitoring of White-shouldered Starlings

A simple Event and Action Plan is shown in Table 6.6.1. Should the Event occur, action in accordance with the Action Plan should be carried out.

There was no recorded event in the reporting month.

Table 6.6.1 Event / Action Plan for Monitoring of White-shouldered Starlings

EVENT	ACTION	
	ET Leader	Contractor
Identification of disturbance to breeding White-shouldered Starlings	1. Increase frequency of monitoring to twice weekly	1. Check all construction actions and working methods
	2. Notify Site Engineer	2. Submit proposals for remedial action to prevent abandonment of the breeding site.
	3. Review construction activities of previous week.	3. Implement remedial action.
	4. Identify any changes in construction activities in previous week	4. Liaise with ET regarding effectiveness of remedial actions.
	5. Discuss remedial actions with Site Engineer	

6.7 Ecological monitoring Schedule

The next ecological surveys are scheduled on June 2011.

7. Action taken in Event of Exceedence

If the measurements (Noise, Water, Ecology) exceed the action / limit level, exceedance details will be reported and follow-up actions will be taken by relevant parties involved.

During the reporting period there was no exceedance for noise, ecological measurements recorded; therefore no actions were taken.

Total 23 non-compliance events of water quality limits (Turbidity, Suspended Solids and DO) were recorded in this reporting month according to the established level. ET has arranged site investigations for the exceedance events and observed that th no particular observations of defective site activities were found causing the exceedance and such conditions were believed to be attributed by natural fluctuation.

8. Construction waste disposal

It is the contractor's responsibility to ensure that all wastes produced during the construction phase for the drainage improvement works are handled, stored and disposed of in accordance with good waste management practices and EPD's regulation and requirement. Waste materials generated during construction activities, such as construction and demolition (C&D) material, chemical wastes and general refuse, are recommended to be audited at regular intervals to ensure that proper storage, transportation and disposal practices are being implemented.

Contractor has completed the registration of Waste Producer under the Waste Disposal (Chemical Waste)(General) Regulation. The Waste Producer Number, WPN 5213-950-Y2443-03 was assigned by EPD on 12 Aug 2008. The Contractor would be responsible for the implementation of any mitigation measure to minimize waste or redress problems arising from the waste materials.

Table 8.1 is a summary of figures of the construction wastes disposal provided by Contractor.

Table 8.1 Summary of Construction Waste Disposal

Month	Amount of Construction Waste disposed		
	Inert Waste (to Public Fill)	Non-inert Waste (to Landfill)	Chemical Waste (to treatment plant)
1 st to 31 st May 11	62.40	Nil	Nil
Total	36467.26 (ton)	247.43 (ton)	0

9. Status of Permits and Licenses obtained

Table 9.1 is the updated status of environmental related permits/ license obtained for the construction activities

Table 9 .1 Status of Permits and Licenses Obtained

Description	License / Permit No.#	Date of Issue	Date of Expiry	Remarks
Environmental Permit	EP-237/2005/A	05 Mar 2007	--	Issued
Varied Environmental Permit	EP-237/2005/B	23 April 2009	--	Issued
Registration of C&D Waste Producer	7006521	--	--	Issued
Chemical Waste Producer	5213-950-Y2443-03	12 Aug 2008	--	Issued
Construction Noise Permit	N/A	N/A	N/A	N/A
Effluent Discharge License	EP890/W2/XG032 EP890/W2/XG033 EP890/W2/XG034 EP890/W2/XG035 EP890/W2/XG036 EP890/W2/XG037 EP890/W2/XG038 EP890/W2/XG039 EP890/W2/XG040 EP890/W2/XG041	23 Oct 2008	31 Oct 2013	Issued

The contractor implemented various environmental mitigation measures as recommended in the Environmental Permit and Final Mitigation Measures Report. The implemented schedule is presented in Appendix H.

10. Complaint Log

There was no formal complaint received during the reporting month.

	Noise	Water	Ecology	Cultural	Others
May 2011	0	0	0	0	0
Total	0	1	0	0	1

11. Site Environmental Audits

Site Inspection

With an intention to ensure that appropriate environmental protection and pollution control mitigation measures are properly implemented, regular environmental site inspections have been scheduled.

Within the reporting month, site inspections were conducted on 4, 13 and 20, 27 May 2011

A detailed checklist of each site inspection together with comments, relevant photos and maps have been filed and kept. A summary of observation and follow-up action is shown in Table 11.1

Table 11.1 Summary of site inspection

Date	Observations	Advice from ET	Action taken	Closing Date
Nov 10 & 31 Dec 10	Open stockpile of earth material was observed at PNH fish ladder site	Contractor was advised to provide tarpaulin covering to earthy stockpile to prevent erosion and dust generation	Open stockpile of earth material was cleaned.	4 April 11
4, 13, 20, 27 May 11	C&D wastes, site materials and general wastes were observed within site area	Contractor should remove wastes and site materials from the concerned area as soon as possible as works finished	To be followed during next reporting period.	ongoing
18 Mar 11, 4 April 11	Stockpile of earthy Materials were observed without protective measure	Contractor should provide tarpaulin cover to the stockpiles to prevent dust generation	Still outstanding. To be followed during the next reporting period	Ongoing
14, 17 & 27 Jan 11; 9 Feb 11 4 April 11 27 May 11	Site surface was observed to be dry and dusty	Contractor was advised to provide regular water spraying to dusty static area for dust suppression	Follow up action was unsatisfactory and to be followed with the improvement during next reporting period	Ongoing
24, 29 Mar 11	Refer to the complaint received. Orange meshes were still observed and deposited within LTT bypass channel.	Contractor was recommended to remove those meshes acting as identification of site boundary since it is not necessary at this stage.	Materials forming the fencings were segregated for further disposal and reuse as disposal by Contractor	30 Mar 11

11.2 Compliance with legal and Contractual requirement

ET leader has reviewed the progress and programme of the works to check any relevant environmental laws has not violated.

11.3 Environmental Complaint and follow up actions

During this reporting period, there was no documented complaint received. Therefore, follow up actions for the environmental complaint is not required.

Findings of monthly survey was still pending therefore relevant was not provided in this reporting month.

12. Future key issues

Landscaping and installation of railing would be major site activities to be carried out in the upcoming month. Although environmental impact arisen from those activities would be expected to be minimal, Contractor was still reminded to pay serious attention to the following key issues:

- Dust generation due to handling of earthy material and dusty site surface.
- Housekeeping of site, such as stockpiling of C&D waste and earthy material.
- Removal of wastes as part of site clearance and evacuation.

Contractor was recommended to provide tarpaulin coverings to all earthy stockpiles on site. Dusty static area should be dampened regularly to avoid dust generation.

Contractor should also prevent excessive storage of wastes on site. Wastes should be collected and disposed to designated public fill.

13. Conclusions

Reconstruction of EVA on top of the PNH Box Culvert, landscaping works and railing installation were major site activities being carried out within this reporting period.

Regular site meetings and inspection audits led by the seniors for discussing site environmental matters were held among Project Proponent, Contractor and the ET on weekly basis. Also monthly site meeting and inspection audits with the above parties and IEC were carried out on 27 May 11.

For noise level monitoring, all results were within the established A/L limits.

For post-construction water quality monitoring, total 23 non-compliance events of water quality limits (Turbidity, Suspended Solids and DO) were recorded in this reporting month according to the established level. ET has arranged site investigations for the exceedance events and observed that no particular observations of defective site activities were found causing the exceedance and such conditions were believed to be attributed by natural fluctuation.

During ecological monitoring survey, no White-shouldered Starling was recorded breeding in the watch tower. The breeding season of White-shouldered Starling in this year has not begun. The absence of nesting of White-shouldered Starling in the watch tower did not seem to be related to construction works in Luk Tei Tong River. A bird species nests in village houses should be to certain extent disturbance tolerant.

No bird was observed entering the watchtower since the monitoring surveys commenced in August 2008. Also, no breeding was recorded in the baseline survey in September 2007. It appears that the birds do not prefer to roost or nest in the watch tower

Also, there were not any notifications of summons recorded during the reporting period. Furthermore, there were not any formal prosecution and complaints recorded.

ET has reminded the contractor to provide environmental pollution control measures wherever necessary; and to keep a good environmental management at site practice.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement.

Appendix A

Construction

Programmer and

Location plan

Appendix B Key Personal Contact information chart

Organization Name	Role	Title	Name	Telephone	Fax Number
Drainage Service Department	Project Proponent	Engineering Representative	Mr. Chan Wai Hong	2594 7464	2827 8700
Allied Environmental Consultants Limited	Independent Environmental Checker (IEC)	Principal Consultant	Ms. Grace Kwok	2815 7028	2815 5399
Yick-Hing Construction Company Limited	Main Contractor	Senior Project Manager	Mr. Liu Kai Choi	2394 4988	2787 4890
Environmental Pioneers & Solutions Limited	Environmental Team (ET)	Environmental Team Leader	Ms. Patricia Chung	2965 0888	2856 2010

Appendix C

Calibration Certificates for Measuring Equipments



CERTIFICATE OF CALIBRATION

Certificate No.: 11CA0117 01-02

Page: 1 of 2

Item tested

Description: Acoustical Calibrator (Class 1)
Manufacturer: Castle
Type/Model No.: GA607
Serial/Equipment No.: 039543
Adaptors used: -

Item submitted by

Customer: Geotechnics & Concrete Engineering (H.K.) Ltd.
Address of Customer: 6 Ko Shan Rd., Ground FL., Hung Hom, Kowloon, Hong Kong
Request No.: RS/11/010-PO
Date of request: 17-Jan-2011

Date of test: 20-Jan-2011

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2412857	02-Jul-2011	SCL
Preamplifier	B&K 2673	2239857	14-Dec-2011	CEPREI
Measuring amplifier	B&K 2610	2346941	15-Dec-2011	CEPREI
Signal generator	DS 360	61227	24-Jun-2011	CEPREI
Digital multi-meter	34401A	US36087050	09-Dec-2011	CEPREI
Audio analyzer	8903B	GB41300350	28-Jun-2011	CEPREI
Universal counter	53132A	MY40003662	05-Jul-2011	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1000 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results


Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:


Huang Jian Min/Feng Jun Qi

Date: 21-Jan-2011

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 11CA0117 01-02 Page: 2 of 2

1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	Estimated Uncertainty dB
1000	94.00	94.31	0.10

(Output level in dB re 20 μ Pa)

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz **STF = 0.001 dB**
Estimated uncertainty 0.005 dB

3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz **Actual Frequency = 1000.1 Hz**
Estimated uncertainty 0.1 Hz Coverage factor k = 2.2

4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz **TND = 3.2%**
Estimated uncertainty 0.7%

The uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95 %. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by: C.Y. Fung
Date: 20-Jan-2011

Checked by:
Date: 21-Jan-2011

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



CERTIFICATE OF CALIBRATION

Certificate No.: 11CA0117 01-01 Page 1 of 2

Item tested

Description:	Sound Level Meter (Type 1)	,	Microphone
Manufacturer:	ACO, Japan	,	ACO, Japan
Type/Model No.:	6224	,	7146
Serial/Equipment No.:	100104	,	39967
Adaptors used:	-	,	-

Item submitted by

Customer Name: Geotechnics & Concrete Engineering (H.K.) Ltd.
Address of Customer: 6 Ko Shan Rd., Ground FL., Hung Hom, Kowloon, Hong Kong
Request No.: RS/11/010-PO
Date of request: 17-Jan-2011

Date of test: 20-Jan-2011

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	10-Jan-2012	CIGISMEC
Signal generator	DS 360	33873	28-Jun-2011	CEPREI
Signal generator	DS 360	61227	24-Jun-2011	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1000 ± 5 hPa

Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of $\pm 20\%$.
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responses of the Sound Level Meter.


Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.


Actual Measurement data are documented on worksheets.

Approved Signatory:


Huang Jian-Min/Feng Jun Qi

Date: 21-Jan-2011

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 11CA0117 01-01

Page 2 of 2

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Uncertainty (dB) / Coverage Factor	
Self-generated noise	A	Pass	0.3	
	C	Pass	1.0	2.1
	Lin	Pass	1.5	2.2
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Frequency weightings			
Time weightings	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Peak response	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
	Time weighting I			
Time averaging	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
Pulse range	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
	Sound exposure level			
Overload indication	Single burst 10 ms at 4 kHz	Pass	0.4	
	SPL	Pass	0.4	
	Leq	Pass	0.3	
		Pass	0.4	

2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Uncertainty (dB) / Coverage Factor	
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

3, Response to associated sound calibrator

N/A

The uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95 %. A coverage factor of 2 is assumed unless explicitly stated.

- End -

Calibrated by: C.Y. Fung
Date: 20-Jan-2011

Checked by: 
Date: 21-Jan-2011

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



Report for Calibration of Hand-held Water Quality Meter WQC-24

Calibration Reference No. : GCE/CHE/WQC/2011-1

Client : ENVIRONMENTAL PIONEER AND SOLUTION LIMITED

Equipment No. : WQC-24 Location : Mui Wo Site

Manufacturer : DKK-TOA Serial No.: 640274

Calibration Date : 01 to 04-03-2011 Due Date : 01-06-2011

Criterion: (Repeatability, Linearity)

pH : Both within ± 0.05 pH
 Dissolved oxygen : Both within ± 0.1 mg/L
 Electric conductivity : Both within $\pm 1\%$ FS
 Turbidity : Repeatability : within $\pm 3\%$ FS
 Temperature : Repeatability $\pm 0.25^\circ\text{C}$; Linearity $\pm 0.5^\circ\text{C}$; (Ambient $5\sim 45^\circ\text{C}$)

Electric Conductivity (Salinity converted from EC):

(Reference : APHA 20ed 2510 B, ISO 7888 - 1985 (E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Concentration of KCl Standard Solution (M)	Reference conductivity value at 25.0°C	Indicated value by meter	Linearity (R^2)
0	0.0 mS/m*	0.0 mS/m	1.0000
0.001	14.7 mS/m	15.3 mS/m	
0.005	71.8 mS/m	72.3 mS/m	Acceptance Criterion $R^2 > 0.995$ Within $\pm 1\%$ F.S. against calibration standard value 71.8 mS/m, 0.667 S/m and 5.87 S/m.
0.01	0.141 S/m	0.145 S/m	
0.05	0.667 S/m	0.671 S/m	
0.1	1.29 S/m	1.30 S/m	
0.5	5.87 S/m	5.89 S/m	
Repeatability	1 st time	0.00, 5.89 S/m	Within $\pm 1\%$ F.S. against average value
	2 nd time	0.00, 5.89 S/m	
	3 rd time	0.00, 5.89 S/m	
	Ave.:	0.00, 5.89 S/m	

* $1 \text{ S/m} = 10^4 \mu\text{mhos/cm} = 10^3 \text{ mS/m}$

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Dissolved Oxygen:

(Reference : APHA 20ed 4500-O B&C, ISO 5814:1990(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

DO value evaluated by Iodometric Method (mg/L)		Indicated value by meter (mg/L)	Linearity (R ²)
0.00		0.00	0.9999
2.95		3.02	
5.42		5.50	Acceptance Criterion
8.62		8.68	R ² > 0.995 Within ± 0.1 mg/L against standard value
10.27		10.35	
13.12		13.06	
Repeatability	1 st time	0.00 , 8.70	Within ± 0.1 mg/L against average value
	2 nd time	0.00 , 8.65	
	3 rd time	0.00 , 8.68	
	0.00 , 8.62	Ave.: 0.00 , 8.68	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

pH Value:

(Reference : APHA 20ed 4500-H⁺ B, ISO 10523:1994(E) and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

pH buffer for Meter Calibration (20°C)	Input value (pH buffer) (20°C)	Indicated pH value by meter (20°C)	Linearity (R ²)
pH = 4.00	1.67	1.71	0.9999
pH = 6.88	4.00	4.03	Acceptance Criterion
pH = 7.00	6.88	6.89	R ² > 0.995 Within ± 0.05 pH against standard value
pH = 9.22	7.00	7.02	
pH = 10.00	7.43	7.45	
	9.22	9.19	
	10.00	9.96	
	12.64	12.67	Within ± 0.05 pH against average value
Repeatability	1 st time	4.03 , 9.97	
	2 nd time	4.03 , 9.96	
	3 rd time	4.02 , 9.95	
	pH 4.00 , 10.00	Ave.: 4.03 , 9.96	

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.



Temperature:

(Reference : APHA 20ed 2550 B, In-house method and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Setting Temperature (°C)	Indicated value by meter (°C)		Linearity (R ²)
5.0	4.6		0.9997
15.0	15.2		
25.0	25.4		Acceptance Criterion R ² > 0.995 Within ± 0.5°C against standard value
35.0	34.7		
45.0	45.3		
55.0	55.3		
Repeatability	1 st time	15.3 , 45.4	Within ± 0.25°C against average value
	2 nd time	15.1 , 45.3	
	3 rd time	15.2 , 45.2	
	15.0 , 45.0		

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.


Turbidity:

(Reference : APHA 20ed 2130 B and DKK-TOA Hand-held Water Quality Meter WQC-24 Instruction Manual)

Formazin Standards (NTU)	Indicated value by meter (NTU)		Linearity (R ²)
0.0	0.0		1.0000
20.0	20.7		Acceptance Criterion R ² > 0.995 Within ± 3% F.S. against span calibration value 100, 400 and 800 NTU
100.0	102.2		
400.0	401.7		
800.0	802.1		
Repeatability	1 st time	0.0 , 801.9	Within ± 3% F.S. against average value
	2 nd time	0.0 , 802.1	
	3 rd time	0.0 , 802.4	
	0.0 , 800.0		

Remark: For repeatability, the maximum difference from the average value of 3 measurements was taken.

Comments : Pass, (comply with the criteria)

Tested by : Fong Ka Lun Certified by : 
 Gu Chin
 Chemist

Checked by : Gu Chin Date : 4-3-2011

Appendix D1 Plant species recorded at Pak Ngan Heung River (N)

<i>Species</i>	Habit	Native	Relative	Occurrence	
			Abundance	PNH3	PNH4
<i>Acacia confusa</i>	tree	no	occasional		+
<i>Achyranthes aspera</i>	herb	yes	scarce		+
<i>Ageratum conyzoides</i>	herb	yes	scarce		+
<i>Alangium chinensis</i>	tree	yes	scarce		+
<i>Alocasia macrorrhiza</i>	herb	yes	occasional		+
<i>Amaranthus viridis</i>	herb	yes	scarce		+
<i>Annona squamosa</i>	tree	no	scarce		+
<i>Bidens pilosa</i>	herb	no	occasional		+
<i>Bridelia tomentosa</i>	tree	yes	scarce		+
<i>Celosia argentea</i>	herb	yes	scarce		+
<i>Celtis sinensis</i>	tree	yes	scarce		+
<i>Cinnamomum camphora</i>	tree	yes	scarce		+
<i>Cleistocalyx operculata</i>	tree	yes	scarce		+
<i>Cocculus orbiculatus</i>	climber	yes	scarce		+
<i>Colocasia esculenta</i>	herb	no	scarce		+
<i>Commelina sp.</i>	herb	yes	scarce		+
<i>Conyza canadensis</i>	herb	no	scarce		+
<i>Crassocephalum crepidioides</i>	herb	yes	scarce		+
<i>Dactyloctenium aegyptium</i>	grass	yes	scarce		+
<i>Dimocarpus longan</i>	tree	no	occasional		+
<i>Emilia sonchifolia</i>	herb	yes	scarce		+
<i>Eupatorium catarium</i>	herb	no	scarce		+
<i>Ficus hispida</i>	tree	yes	scarce		+
<i>Ficus microcarpa</i>	tree	yes	scarce		+
<i>Ficus superba</i>	tree	yes	occasional		+
<i>Fimbristylis sp.</i>	herb	yes	scarce		+
<i>Gardenia jasminoides</i>	shrub	yes	occasional		+
<i>Hedychium coronarium</i>	herb	no	occasional		+
<i>Ipomoea cairica</i>	climber	no	scarce		+
<i>Liquidambar formosana</i>	tree	yes	occasional		+
<i>Lygodium japonicum</i>	fern	yes	scarce		+
<i>Macaranga tanarius</i>	tree	yes	occasional		+

<i>Species</i>	Habit	Native	Relative	Occurrence	
			Abundance	PNH3	PNH4
<i>Mallotus paniculatus</i>	tree	yes	occasional		+
<i>Microstegium ciliatum</i>	grass	yes	common		+
<i>Mikania micrantha</i>	climber	no	occasional	+	+
<i>Mimosa pudica</i>	herb	no	scarce		+
<i>Neyraudia reynaudiana</i>	grass	yes	scarce		+
<i>Oxalis corymbosa</i>	herb	yes	scarce		+
<i>Panicum maximum</i>	grass	no	scarce		+
<i>Paspalum paspaloides</i>	grass	yes	scarce		+
<i>Phyllanthus urinaria</i>	shrub	yes	scarce		+
<i>Polygonum hydropiper</i>	herb	yes	scarce		+
<i>Pteris ensiformis</i>	fern	yes	scarce		+
<i>Pteris vittata</i>	fern	yes	scarce		+
<i>Rhus hypoleuca</i>	tree	yes	scarce		+
<i>Sonchus oleraceus</i>	herb	yes	scarce		+
<i>Stephania longa</i>	climber	yes	scarce		+
<i>Sterculia lanceolata</i>	tree	yes	scarce		+
<i>Urena lobata</i>	herb	yes	scarce		+
<i>Vernonia cinerea</i>	herb	yes	scarce		+
<i>Wedelia triloba</i>	climber	no	scarce		+
<i>Youngia japonica</i>	herb	yes	scarce		+

Appendix D2 Plant species recorded at Pak Ngan Heung River (S)

Species	Habit	Native	Relative	Occurrence	
			Abundance	PNH1	PNH2
<i>Ficus superba</i>	tree	yes	occasional		+
<i>Ipomoea cairica</i>	climber	yes	occasional		+
<i>Kandelia obovata</i>	tree	yes	scarce	+	
<i>Lantana camara</i>	shrub	no	scarce		+
<i>Panicum maximum</i>	grass	no	common		+

Appendix D3 Plant species recorded at Luk Tei Tong River

Species	Habit	Native	Relative	Occurrence				
			Abundance	LLT1	LLT2	LLT3	LLT4	LLT5
<i>Acanthus ilicifolius</i>	shrub	yes	scarce		+			
<i>Bidens pilosa</i>	herb	no	scarce	+		+		
<i>Pueraria phaseoloides</i>	climber	yes	scarce			+		
<i>Celtis sinensis</i>	tree	yes	scarce	+				
<i>Ficus hispida</i>	tree	yes	scarce	+				
<i>Ficus microcarpa</i>	tree	yes	scarce	+				
<i>Ficus superba</i>	tree	yes	scarce	+				
<i>Hibiscus tiliaceus</i>	tree	yes	scarce	+				
<i>Kandelia obovata</i>	tree	yes	occasional		+			
<i>Leucaena leucocephala</i>	tree	no	scarce	+				
<i>Macaranga tanarius</i>	tree	yes	scarce	+				
<i>Mikania micrantha</i>	climber	no	scarce	+				
<i>Neyraudia reynaudiana</i>	grass	yes	scarce	+		+	+	
<i>Panicum maximum</i>	grass	no	scarce	+				
<i>Rhynchelytrum repens</i>	grass	no	scarce	+				
<i>Saccharum arundinaceum</i>	grass	yes	scarce	+				
<i>Solanum nigrum</i>	herb	no	scarce	+				

Appendix D4

Ecological Water Monitoring Results (on-site measurements)

Environmental Pioneers & Solutions Limited
Ecological Water Quality Monitoring - Summary of On-site measurement results

Date of Sampling: 27/5/2011

Weather Condition: Sunny

Monitoring Location	WE1			WE2			WE3			WE4			WE5			WE6		
Time (hhmm)	1200			1150			1100			1120			1130			1220		
Tide Mode	ebb			ebb			ebb			ebb			ebb			ebb		
River Condition	Normal			Normal			Normal			Normal			Normal			Normal		
Water Depth (m)	< 1.0			< 1.0			< 1.0			< 1.0			< 1.0			< 1.0		
pH value	6.07			7.07			7.30			6.49			6.68			7.69		
Temperature (oC)	25.4			26.5			25.3			27.3			29.3			28.3		
Salinity (ppt)	0.0			0.0			0.6			13.9			3.8			0.1		
Conductivity (s/m)	7.9			14.6			1.1			2.1			0.7			20.3		
Water flow (m/s)	1.100			<0.1			0.100			0.100			0.100			<0.1		
Turbidity (NTU)	0.0	0.0	Average	0.0	0.0	Average	0.0	0.0	Average	0.8	0.8	Average	2.8	2.8	Average	0.4	0.4	Average
			0.00			0.00			0.00			0.8			2.80			0.4
DO (mg/l)	7.25	7.25	Average	7.96	7.98	Average	7.99	7.97	Average	6.04	6.04	Average	6.84	6.81	Average	10.70	10.70	Average
			7.25			7.97			7.98			6.04			6.83			10.70
DO Saturation (%)	88	88	Average	99	99	Average	98	98	Average	81	81	Average	91	91	Average	138	138	Average
			88			99			98			81			91			138

Name: Allen Signature: Allen Chan Date: 27/5/2011 remark or observation: _____

Appendix D5

Ecological Water Monitoring Results (lab report)



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC110501033 Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 12:20 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE6 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU APHA 20ed 2120 B	--
Turbidity	NTU APHA 20ed 2130 B	--
Conductivity at 25°C	µS/cm APHA 20ed 2510 B	--
Salinity	g/L APHA 20ed 2520 B	--
Nitrogen (Ammonia)	mg/L APHA 20ed 4500-NH ₃ D	0.08
	mg/L APHA 20ed 4500-NH ₃ E	--
	mg/L APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate)	mg/L APHA 20ed 4500-NO ₃ ⁻ E	0.11
Phosphorus	mg/L APHA 20ed 4500-P D	0.09
Biochemical Oxygen Demand (BOD ₅)	mg/L APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD)	mg/L APHA 20ed 5220 D	--
Total Suspended Solid	mg/L APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE6.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC110501025

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 12:20 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE6

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.08
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.11
Phosphorus mg/L	APHA 20ed 4500-P D	0.08
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	< 1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE6.

---- End ----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110501017

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 27-05-2011

W.O. No.* : --

Contract No.* : --

Date Completed : 02-06-2011

GCE Serial No. : WQM052011

Sampling Date* : 27-05-2011 / 11:30

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE5 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.78
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.35
Phosphorus mg/L	APHA 20ed 4500-P D	0.20
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	3
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE5.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By

Name

Gu Chin

Checked By : Gu Chin

Post

Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110501009

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 27-05-2011

W.O. No.* : --

Contract No.* : --

Date Completed : 02-06-2011

GCE Serial No. : WQM052011

Sampling Date* : 27-05-2011 / 11:30

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE5

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	1.79
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.34
Phosphorus mg/L	APHA 20ed 4500-P D	0.19
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	2
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE5.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500998

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 11:20 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE4 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.25
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	1.39
Phosphorus mg/L	APHA 20ed 4500-P D	0.18
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE4.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500980

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 27-05-2011

W.O. No.* : --

Contract No.* : --

Date Completed : 02-06-2011

GCE Serial No. : WQM052011

Sampling Date* : 27-05-2011 / 11:20

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE4

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.25
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	1.39
Phosphorus mg/L	APHA 20ed 4500-P D	0.19
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE4.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 

Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500972

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited

Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 27-05-2011

W.O. No.* : --

Contract No.* : --

Date Completed : 02-06-2011

GCE Serial No. : WQM052011

Sampling Date* : 27-05-2011 / 11:00

Sample Type* : River Water

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Sample I.D.* : WE3 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour	TCU	APHA 20ed 2120 B
Turbidity	NTU	APHA 20ed 2130 B
Conductivity at 25°C	µS/cm	APHA 20ed 2510 B
Salinity	g/L	APHA 20ed 2520 B
Nitrogen (Ammonia)	APHA 20ed 4500-NH ₃ D	0.67
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate)	mg/L	APHA 20ed 4500-NO ₃ ⁻ E
Phosphorus	mg/L	APHA 20ed 4500-P D
Biochemical Oxygen Demand (BOD ₅)	mg/L	APHA 20ed 5210 B
Chemical Oxygen Demand (COD)	mg/L	APHA 20ed 5220 D
Total Suspended Solid	mg/L	APHA 20ed 2540 D

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE3.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 

Checked By : Gu Chin

Name : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500964

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of
 Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 11:00 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE3

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.68
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.52
Phosphorus mg/L	APHA 20ed 4500-P D	0.12
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	2
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE3.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500956

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 11:50 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE2 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.16
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.35
Phosphorus mg/L	APHA 20ed 4500-P D	0.09
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE2.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500948

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011 / 11:50 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE2

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.16
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.34
Phosphorus mg/L	APHA 20ed 4500-P D	0.08
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	<1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE2.

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Report No. : GCC110500930 Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011/12:00 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE1 Duplicate

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.09
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.20
Phosphorus mg/L	APHA 20ed 4500-P D	0.06
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE1

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER

Page 1 of 1

Report No. : GCC110500922

Date of Issue : 14-06-2010

Client* : Environmental Pioneers & Solutions Limited Order Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 27-05-2011

W.O. No.* : -- Contract No.* : -- Date Completed : 02-06-2011

GCE Serial No. : WQM052011 Sampling Date* : 27-05-2011/12:00 Sample Type* : River Water

GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258 Sample I.D.* : WE1

Description : River Water

DESCRIPTION	TEST REFERENCE (In-House Method based on)	TEST RESULT
Appearance	APHA 20ed 2110	--
Odour	APHA 20ed 2150 B	Odour Characteristics : --
		Threshold Odour Number (TON) : --
pH Value at temperature [] °C	APHA 20ed 4500-H ⁺ B	--
Colour TCU	APHA 20ed 2120 B	--
Turbidity NTU	APHA 20ed 2130 B	--
Conductivity at 25°C μS/cm	APHA 20ed 2510 B	--
Salinity g/L	APHA 20ed 2520 B	--
Nitrogen (Ammonia) mg/L	APHA 20ed 4500-NH ₃ D	0.08
	APHA 20ed 4500-NH ₃ E	--
	APHA 18ed 4500-NH ₃ C	--
Nitrogen (Nitrate) mg/L	APHA 20ed 4500-NO ₃ ⁻ E	0.20
Phosphorus mg/L	APHA 20ed 4500-P D	0.06
Biochemical Oxygen Demand (BOD ₅) mg/L	APHA 20ed 5210 B	1
Chemical Oxygen Demand (COD) mg/L	APHA 20ed 5220 D	--
Total Suspended Solid mg/L	APHA 20ed 2540 D	--

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Sample received on 27 May 2011

REMARKS : Sample Location WE1

----- End -----

Tested By : K.L. Fong, C.S. Chan

Certified By : 
 Name : Gu Chin

Checked By : Gu Chin

Post : Chemist

Appendix E

Construction Noise Monitoring Data Sheet



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		6/5/2011	
Measurement Start Time (hhmm)		13:25	12:50
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.1	0.1
Measurement Results	L90 (dB(A))	43.4	39.1
	L10 (dB(A))	57.3	48.3
	Leq (dB(A))	55.9	47.5
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise 2. Traffic noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 6/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		6/5/2011	
Measurement Start Time (hhmm)		12:15	11:40
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.2	0.2
Measurement Results	L90 (dB(A))	38.7	40.3
	L10 (dB(A))	52.3	51.0
	Leq (dB(A))	49.9	48.7
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 6/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		13/5/2011	
Measurement Start Time (hhmm)		14:45	14:10
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.4	0.3
Measurement Results	L90 (dB(A))	40.8	40.9
	L10 (dB(A))	56.7	50.8
	Leq (dB(A))	54.9	47.6
Weather condition:		Rain	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during measurement.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise 2. Traffic noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 13/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		13/5/2011	
Measurement Start Time (hhmm)		13:35	13:00
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.4	0.4
Measurement Results	L90 (dB(A))	41.6	37.2
	L10 (dB(A))	59.4	51.6
	Leq (dB(A))	57.3	46.5
Weather condition:		Rain	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 13/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		20/5/2011	
Measurement Start Time (hhmm)		12:10	12:45
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.2	0.2
Measurement Results	L90 (dB(A))	41.2	43.5
	L10 (dB(A))	54.4	57.1
	Leq (dB(A))	67.8	54.1
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise 2. Traffic noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 20/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		20/5/2011	
Measurement Start Time (hhmm)		11:35	10:55
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.1	0.1
Measurement Results	L90 (dB(A))	41.7	40.8
	L10 (dB(A))	60.8	52.0
	Leq (dB(A))	56.5	48.8
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 20/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N1	N2
Description of Location		Façade	Façade
Date of Monitoring		27/5/2011	
Measurement Start Time (hhmm)		12:45	12:10
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.3	0.2
Measurement Results	L90 (dB(A))	45.3	43.9
	L10 (dB(A))	56.8	58.1
	Leq (dB(A))	55.1	54.8
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 27/5/2011



大成環境科技拓展有限公司
Environmental Pioneers and Solutions Limited

Construction Noise Monitoring Data Sheet

Monitoring Location		N3	N4
Description of Location		Freefield	Facade
Date of Monitoring		27/5/2011	
Measurement Start Time (hhmm)		11:35	11:00
Measurement Time Length (mins.)		30 mins	
Noise Meter Model/ Identification		ACO Japan, model 6224	
Calibrator Model/ Identification		Castle Group, GA607	
Wind Speed (m/s)		0.4	0.3
Measurement Results	L90 (dB(A))	39.9	39.6
	L10 (dB(A))	57.9	53.6
	Leq (dB(A))	54.2	52.6
Weather condition:		Sunny	
Major Construction Noise Source(s) During Monitoring		No construction work has been carried out during monitoring.	No construction work has been carried out during monitoring.
Other Noise Source(s) During Monitoring		1. Public noise 2. Traffic noise 3. Other construction work noise	1. Public noise
Remarks			

Name & Designation

Signature

Date:

Prepared by: Allen Chan Allen 27/5/2011

Appendix F1

Water Quality

Monitoring Data Sheet

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 3/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1240			1250			1300			1230			1150			1200			1210		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	7.31			7.76			7.01			7.26			7.42			7.63			7.21		
Temperature (oC)	25.9			25.6			26.3			26.2			26.4			25.8			26.2		
Salinity (ppt)	10.8			22.7			23.1			24.2			0.0			0.0			0.0		
Turbidity (NTU)	3.2	3.2	Average	0.0	0.0	Average	6.3	6.3	Average	7.1	7.1	Average	12.3	12.3	Average	0.0	0.0	Average	9.8	9.8	Average
			3.2						0.0						6.3						7.1
DO (mg/l)	8.19	8.19	Average	8.73	8.74	Average	8.80	8.82	Average	8.01	7.99	Average	8.63	8.64	Average	8.73	8.74	Average	6.91	6.89	Average
			8.19						8.74						8.81						8.00
DO Saturation (%)	103	103	Average	109	109	Average	109	109	Average	101	101	Average	107	107	Average	108	108	Average	85	85	Average
			103						109						109						101

Name Signature Date
 Prepared By: Allen Chan Allen 3/5/2011

remark or _____
 observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 4/5/2011

Sunny

Monitoring Location	1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1240			1250			1300			1230			1150			1200			1210		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.2			<1			<1			<1		
pH value	7.64			8.01			7.34			7.55			7.43			7.98			7.31		
Temperature (oC)	26.2			25.9			26.2			26.3			26.3			25.1			26.2		
Salinity (ppt)	16.7			23.1			24.5			25.2			0.0			0.0			15.0		
Turbidity (NTU)	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.9	0.8	Average 0.9	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0
DO (mg/l)	8.30	8.31	Average 8.31	9.02	8.98	Average 9.00	8.80	8.81	Average 8.81	8.05	8.05	Average 8.05	9.18	9.19	Average 9.19	9.13	9.16	Average 9.15	6.72	6.74	Average 6.73
DO Saturation (%)	104	104	Average 104	111	111	Average 111	109	109	Average 109	101	101	Average 101	114	114	Average 114	112	112	Average 112	83	83	Average 83

Name: Allen Chan Signature: Allen Date: 4/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 6/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1430			1440			1450			1420			1510			1520			1530		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	8.03			7.11			7.59			7.99			8.14			7.34			7.29		
Temperature (oC)	29.4			27.8			29.3			29.1			29.0			29.9			29.6		
Salinity (ppt)	13.7			15.6			23.1			24.8			0.0			0.0			18.4		
Turbidity (NTU)	0.0	0.0	Average	2.8	2.8	Average	5.7	5.7	Average	4.0	4.0	Average	0.0	0.0	Average	0.0	0.0	Average	12.2	12.2	Average
			0.0			2.8			5.7			4.0			0.0			0.0			12.2
DO (mg/l)	7.94	7.91	Average	8.72	8.70	Average	9.22	9.20	Average	9.43	9.44	Average	9.30	9.30	Average	9.17	9.19	Average	9.31	9.30	Average
			7.93			8.71			9.21			9.44			9.30			9.18			9.31
DO Saturation (%)	104	104	Average	112	112	Average	122	122	Average	123	123	Average	120	120	Average	117	117	Average	119	119	Average
			104			112			122			123			120			117			119

Name Signature Date
Prepared By: Allen Chan Allen 6/5/2011

remark or
observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 9/5/2011

Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1510			1520			1530			1500			1420			1430			1440		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	8.11			8.11			7.84			8.03			7.49			7.16			7.58		
Temperature (oC)	30.3			29.0			29.5			29.1			27.5			27.1			29.2		
Salinity (ppt)	21.6			22.6			25.0			25.6			0.0			0.0			18.3		
Turbidity (NTU)	4.2	4.2	Average	2.0	2.0	Average	3.6	3.6	Average	5.2	5.2	Average	5.7	5.7	Average	0.0	0.0	Average	10.9	10.9	Average
			4.2			2.0			3.6			5.2			5.7			0.0			10.9
DO (mg/l)	9.24	9.26	Average	9.67	9.68	Average	9.13	9.13	Average	9.76	9.78	Average	9.28	9.29	Average	9.60	9.60	Average	9.23	9.23	Average
			9.25			9.68			9.13			9.77			9.29			9.60			9.23
DO Saturation (%)	122	122	Average	126	126	Average	120	120	Average	127	127	Average	118	118	Average	123	123	Average	121	121	Average
			122			126			120			127			118			123			121

Name: Allen Chan Signature: Allen Date: 9/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 11/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1630			1620			1610			1640			1530			1540			1550		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	8.41			8.23			7.96			7.99			8.01			7.64			7.09		
Temperature (oC)	32.6			31.2			31.4			30.8			31.0			28.6			33.8		
Salinity (ppt)	18.6			11.5			21.4			25.6			0.0			0.0			10.5		
Turbidity (NTU)	6.5	6.5	Average 6.5	2.6	2.6	Average 2.6	9.7	9.7	Average 9.7	6.2	9.2	Average 7.7	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	10.4	10.4	Average 10.4
DO (mg/l)	9.61	9.61	Average 9.61	9.21	9.22	Average 9.22	8.94	8.96	Average 8.95	8.99	8.97	Average 8.98	8.36	8.35	Average 8.36	8.91	8.91	Average 8.91	9.01	9.01	Average 9.01
DO Saturation (%)	135	135	Average 135	131	131	Average 131	129	129	Average 129	129	129	Average 129	118	118	Average 118	125	125	Average 125	130	130	Average 130

Name: Allen Chan Signature: Allen Date: 11/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 13/5/2011

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1050			1100			1110			1040			1130			1140			1150		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	7.07			6.92			6.87			7.16			7.78			6.46			6.58		
Temperature (oC)	27.7			27.1			29.0			28.4			29.6			27.4			26.6		
Salinity (ppt)	0.7			0.4			10.3			16.1			0.0			0.0			0.8		
Turbidity (NTU)	1.3	1.3	Average 1.3	2.1	2.1	Average 2.1	6.0	6.0	Average 6.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	7.7	7.7	Average 7.7
DO (mg/l)	6.54	6.56	Average 6.55	6.52	6.56	Average 6.54	6.56	6.58	Average 6.57	6.16	6.18	Average 6.17	8.72	8.71	Average 8.72	8.12	8.12	Average 8.12	6.16	6.18	Average 6.17
DO Saturation (%)	83	83	Average 83	82	82	Average 82	90	90	Average 90	87	87	Average 87	113	113	Average 113	100	100	Average 100	86	86	Average 86

Name: Allen Chan Signature: Allen Date: 13/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 16/5/2011

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1130			1140			1150			1120			1210			1220			1230		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			< 1			< 1			1.3			< 1			< 1			< 1		
pH value	7.15			7.04			7.12			6.90			7.27			6.36			6.18		
Temperature (oC)	28.6			27.2			28.5			27.4			25.1			26.9			28.5		
Salinity (ppt)	8.9			10.7			19.4			20.5			0.0			0.0			10.5		
Turbidity (NTU)	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	7.0	7.0	Average 7.0
DO (mg/l)	7.92	7.94	Average 7.93	6.93	6.90	Average 6.92	6.85	6.81	Average 6.83	6.73	6.73	Average 6.73	8.62	8.61	Average 8.62	9.63	9.61	Average 9.62	6.66	6.66	Average 6.66
DO Saturation (%)	107	107	Average 107	93	93	Average 93	98	98	Average 98	96	96	Average 96	105	105	Average 105	114	114	Average 114	91	91	Average 91

Name: Allen Chan Signature: Allen Date: 16/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 18/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1230			1240			1250			1220			1140			1150			1200		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			1.4			< 1			< 1			< 1		
pH value	7.36			7.14			7.33			7.10			7.97			8.12			6.94		
Temperature (oC)	26.9			26.5			27.4			26.5			25.6			26.0			26.4		
Salinity (ppt)	20.3			20.1			25.4			24.4			0.0			0.0			17.6		
Turbidity (NTU)	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.9	0.9	Average 0.9	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0
DO (mg/l)	7.13	7.13	Average 7.13	7.71	7.71	Average 7.71	7.66	7.64	Average 7.65	7.62	7.62	Average 7.62	8.88	8.88	Average 8.88	9.14	9.14	Average 9.14	6.03	6.03	Average 6.03
DO Saturation (%)	101	101	Average 101	109	109	Average 109	112	112	Average 112	111	111	Average 111	109	109	Average 109	121	121	Average 121	87	87	Average 87

Name: Allen Chan Signature: Allen Date: 18/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 20/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1320			1330			1340			1310			1400			1410			1420		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			1.4			< 1			< 1			< 1		
pH value	7.04			7.25			7.40			7.05			8.08			8.22			7.22		
Temperature (oC)	28.3			28.4			28.8			28.1			28.5			30.3			29.4		
Salinity (ppt)	19.8			18.1			24.8			24.7			0.7			0.0			21.1		
Turbidity (NTU)	8.4	8.4	Average	1.2	1.1	Average	4.0	3.8	Average	0.0	0.0	Average	7.7	7.5	Average	3.3	3.5	Average	8.9	8.9	Average
			8.4			1.2			3.9			0.0			7.6			3.4			8.9
DO (mg/l)	6.59	6.62	Average	8.04	8.05	Average	8.34	8.31	Average	6.48	6.50	Average	9.82	9.84	Average	9.81	9.80	Average	8.28	8.25	Average
			6.61			8.05			8.33			6.49			9.83			9.81			8.27
DO Saturation (%)	95	95	Average	116	116	Average	126	126	Average	95	95	Average	127	127	Average	127	127	Average	122	122	Average
			95			116			126			95			127			127			122

Name: Allen Chan Signature: Allen Date: 20/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 23/5/2011

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1510			1520			1530			1500			1410			1420			1430		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			< 1			< 1			1.3			< 1			< 1			< 1		
pH value	6.76			7.20			6.65			6.45			6.42			6.30			6.18		
Temperature (oC)	25.4			24.6			26.2			25.8			24.3			24.0			25.5		
Salinity (ppt)	3.5			0.6			9.8			4.9			0.0			0.0			0.3		
Turbidity (NTU)	3.5	3.5	Average 3.5	0.7	0.7	Average 0.7	9.4	9.4	Average 9.4	5.3	5.3	Average 5.3	4.8	4.8	Average 4.8	0.0	0.0	Average 0.0	3.6	3.6	Average 3.6
DO (mg/l)	8.07	8.08	Average 8.08	8.17	8.16	Average 8.17	7.26	7.24	Average 7.25	8.02	8.01	Average 8.02	7.97	7.97	Average 7.97	8.11	8.12	Average 8.12	7.15	7.16	Average 7.16
DO Saturation (%)	100	100	Average 100	99	99	Average 99	95	95	Average 95	103	103	Average 103	95	95	Average 95	97	97	Average 97	87	87	Average 87

Name: Allen Chan Signature: Allen Date: 23/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 24/5/2011

Cloudy

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1550			1600			1610			1540			1500			1510			1520		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	6.56			6.52			6.69			6.89			6.72			6.94			6.62		
Temperature (oC)	24.1			23.9			24.9			25.1			23.1			23.2			24.3		
Salinity (ppt)	5.3			3.0			11.7			16.8			0.0			0.0			1.5		
Turbidity (NTU)	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	4.3	4.3	Average 4.3	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	10.3	10.3	Average 10.3
DO (mg/l)	7.21	7.22	Average 7.22	7.62	7.61	Average 7.62	6.93	6.94	Average 6.94	6.65	6.65	Average 6.65	8.22	8.22	Average 8.22	8.05	8.05	Average 8.05	6.82	6.82	Average 6.82
DO Saturation (%)	89	89	Average 89	92	92	Average 92	89	89	Average 89	89	89	Average 89	96	96	Average 96	95	95	Average 95	83	83	Average 83

Name: Allen Chan Signature: Allen Date: 24/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 27/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1100			1110			1120			1050			1200			1210			1230		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	<1			<1			<1			1.3			<1			<1			<1		
pH value	7.30			6.45			6.49			6.48			6.07			6.61			6.37		
Temperature (oC)	25.3			26.6			27.3			26.2			25.4			25.7			28.2		
Salinity (ppt)	0.6			0.5			13.9			18.4			0.0			0.0			2.0		
Turbidity (NTU)	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.8	0.8	Average 0.8	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	0.0	0.0	Average 0.0	18.8	18.8	Average 18.8
DO (mg/L)	7.99	7.98	Average 7.99	7.67	7.67	Average 7.67	6.04	6.04	Average 6.04	7.00	7.00	Average 7.00	7.25	7.25	Average 7.25	7.12	7.11	Average 7.12	6.14	6.14	Average 6.14
DO Saturation (%)	98	98	Average 98	97	97	Average 97	81	81	Average 81	97	97	Average 97	88	88	Average 88	88	88	Average 88	74	74	Average 74

Name: Allen Chan Signature: Allen Date: 27/5/2011

remark or observation: _____

Environmental Pioneers & Solutions Limited
Water Quality Monitoring - Summary of On-Site Measurement Results

Date of Sampling: 30/5/2011 Sunny

Monitoring Location	M1			M2			M3			M4			C1			C2			C3		
Time (hhmm)	1240			1250			1300			1230			1150			1200			1210		
Tide Mode	mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb			mid-ebb		
River Condition	normal			normal			normal			normal			normal			normal			normal		
Water Depth (m)	< 1			< 1			< 1			1.4			< 1			< 1			< 1		
pH value	8.08			7.61			7.58			8.05			7.51			8.70			6.99		
Temperature (oC)	28.3			26.7			27.8			27.8			27.4			26.3			28.3		
Salinity (ppt)	5.9			13.1			20.6			22.7			0.1			1.0			9.4		
Turbidity (NTU)	7.5	7.5	Average 7.5	2.6	2.6	Average 2.6	6.2	6.2	Average 6.2	7.0	7.0	Average 7.0	4.3	4.3	Average 4.3	0.5	0.5	Average 0.5	10.9	10.9	Average 10.9
DO (mg/l)	8.68	8.66	Average 8.67	8.62	8.64	Average 8.63	9.39	9.39	Average 9.39	9.32	9.48	Average 9.40	8.02	8.01	Average 8.02	9.60	9.62	Average 9.61	8.36	8.35	Average 8.36
DO Saturation (%)	112	112	Average 112	108	108	Average 108	120	120	Average 120	122	122	Average 122	102	102	Average 102	124	124	Average 124	108	108	Average 108

Name Signature Date
 Prepared By: Allen Chan Allen 30/5/2011

remark or observation: _____

Appendix F2

Water Quality

Monitoring Lab report



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500095 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 03-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 04-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08268

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	496	0.4	27.0
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time	03 May 2011 / 11:50			03 May 2011 / 12:00		03 May 2011 / 12:10			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	13.9	13.6	1.6	1.3	8.9	9.2		

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	03 May 2011 / 12:40			03 May 2011 / 12:50		03 May 2011 / 13:00		03 May 2011 / 12:30	
	LOD	Units								
Suspended Solids (SS)	1	mg/L	5.4	5.8	1.6	1.9	8.6	8.6	7.3 8.0	


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500100 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 04-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 05-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	496	497	-0.2	26.4
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	04 May 2011 / 11:50		04 May 2011 / 12:00		04 May 2011 / 12:10			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	2.6	2.0	1.0	1.2	7.3	7.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	04 May 2011 / 12:40		04 May 2011 / 12:50		04 May 2011 / 13:00		04 May 2011 / 12:30	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	3.3	3.6	2.6	2.9	4.2	4.2	5.0 4.7


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

--- End ----

Tested By : C.S. CHAN
 Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500118 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 06-05-2011

W.O. No.* : - Sample Type* : River Water Date Completed : 07-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	498	0.0	27.2
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	05 May 2011 / 15:10		05 May 2011 / 15:20		05 May 2011 / 15:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.6	1.2	2.2	2.3	15.4	15.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	05 May 2011 / 14:30		05 May 2011 / 14:40		05 May 2011 / 14:40		05 May 2011 / 14:20	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.8	1.9	2.3	2.1	5.9	5.6	1.8 2.0


* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : C.S. CHAN

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500126 Date of issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 09-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 10-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	495	496	-0.2	26.4
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
		Sampling Date/Time	09 May 2011 / 14:20		09 May 2011 / 14:30		09 May 2011 / 14:40		
	LOD								
	Units								
Suspended Solids (SS)	1	mg/L	7.8	7.8	<1.0	<1.0	7.9	8.3	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
		Sampling Date/Time	09 May 2011 / 15:10		09 May 2011 / 15:20		09 May 2011 / 15:30		09 May 2011 / 15:00	
	LOD									
	Units									
Suspended Solids (SS)	1	mg/L	6.8	6.7	2.9	2.8	5.2	5.0	5.7	6.3

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

--- End ---

Tested By : C.S. CHAN

Approved Signatory : 
 Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500134 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 11-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 12-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	497	498	-0.2	26.8
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	11 May 2011 / 15:30		11 May 2011 / 15:40		11 May 2011 / 15:50			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.4	1.6	1.4	1.0	13.6	14.4	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	11 May 2011 / 16:30		11 May 2011 / 16:20		11 May 2011 / 16:10		11 May 2011 / 16:40	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	3.9	4.3	2.0	1.5	8.6	8.3	7.0 7.3

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : C.S. CHAN

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500142 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : B/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 13-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 14-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	498	0.0	27.2
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	13 May 2011 / 11:30		13 May 2011 / 11:40		13 May 2011 / 11:50			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.4	1.2	3.2	3.3	9.4	9.0	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	13 May 2011 / 10:50		13 May 2011 / 11:00		13 May 2011 / 11:10		13 May 2011 / 10:40	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	1.8	1.9	2.0	1.8	6.4	6.7	1.8 2.0

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500150

Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited

Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 16-05-2011

W.O. No.* : -- Sample Type* : River Water

Date Completed : 17-05-2011

GCE Serial No. : WQM052011

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	497	497	0.0	26.8
Acceptance Criteria			<2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate			
	Sampling Date/Time	16 May 2011 / 12:10			16 May 2011 / 12:20		16 May 2011 / 12:30			
	LOD	Units								
Suspended Solids (SS)	1	mg/L	2.2	2.6	<1.0	<1.0	8.9	8.5		

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate	
	Sampling Date/Time	16 May 2011 / 11:30			16 May 2011 / 11:40		16 May 2011 / 11:50		16 May 2011 / 11:20	
	LOD	Units								
Suspended Solids (SS)	1	mg/L	2.9	2.3	1.6	1.6	5.3	5.4	4.2	3.9

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500168 Date of Issue : 28-05-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 18-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 19-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	499	496	0.6	28.6
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	18 May 2011 / 11:40		18 May 2011 / 11:50		18 May 2011 / 12:00			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	2.8	2.0	1.9	1.7	4.2	4.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	18 May 2011 / 12:30		18 May 2011 / 12:40		18 May 2011 / 12:50		18 May 2011 / 12:20	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	3.2	2.9	1.2	1.3	3.4	3.2	4.8

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : C.S. CHAN

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500176 Date of Issue : 14-06-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 20-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 21-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08288

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	498	498	0.0	27.2
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	20 May 2011 / 14:00		20 May 2011 / 14:10		20 May 2011 / 14:20			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.8	4.4	3.2	3.3	11.4	11.6	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	20 May 2011 / 13:20		20 May 2011 / 13:30		20 May 2011 / 13:40		20 May 2011 / 13:10	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	6.8	6.9	1.5	1.8	5.9	5.9	1.8 2.0

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

---- End ----

Tested By : C.S. CHAN

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500859 Date of Issue : 14-06-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2008/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 23-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 24-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	499	497	0.4	26.8
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	23 May 2011 / 14:10		23 May 2011 / 14:20		23 May 2011 / 14:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	6.0	5.9	<1.0	<1.0	4.8	4.1	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	23 May 2011 / 15:10		23 May 2011 / 15:20		23 May 2011 / 15:30		23 May 2011 / 15:00	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.0	4.1	<1.0	<1.0	7.4	7.2	5.9 5.8

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Report No. : GCC110500867 Date of Issue : 14-06-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 24-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 25-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	499	496	0.6	27.6
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
		Sampling Date/Time	24 May 2011 / 15:00		24 May 2011 / 15:10		24 May 2011 / 15:20		
	LOD	Units							
Suspended Solids (SS)	1	mg/L	2.5	2.9	<1.0	<1.0	8.2	8.2	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
		Sampling Date/Time	24 May 2011 / 15:50		24 May 2011 / 16:00		24 May 2011 / 16:10		24 May 2011 / 15:40
	LOD	Units							
Suspended Solids (SS)	1	mg/L	3.2	3.2	1.0	1.3	6.8	6.3	3.9 3.5

* : Information provided by client


Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Checked By : GU CHIN

Approved Signatory : 
 Name : GU CHIN
 Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500875

Date of Issue : 14-06-2011

Client* : Environmental Pioneers & Solutions Limited

P.O. Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.

DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon.

Date Started : 27-05-2011

W.O. No.* : --

Sample Type* : River Water

Date Completed : 27-05-2011

GCE Serial No. : WQM052011

GCE Reg. No. : GCE 081096

Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results						
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L		
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	497	498	-0.2	27.6		
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ± 5%	21 ≤ R ≤ 29		
TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	27 May 2011 / 12:00		27 May 2011 / 12:10		27 May 2011 / 12:30			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	2.8	2.8	< 1.0	< 1.0	16.6	16.2	
TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	27 May 2011 / 11:00		27 May 2011 / 11:10		27 May 2011 / 11:20		27 May 2011 / 10:50	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	3.3	3.8	1.0	1.1	5.0	4.7	5.3

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : Location M1 & WE3 and Location M3 & WE4 are the same location.

---- End ----

Tested By : K.L. FONG

Approved Signatory :

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist



TEST REPORT ON ENVIRONMENTAL ANALYSIS OF WATER AND WASTEWATER

Page 1 of 1

Report No. : GCC110500891 Date of Issue : 14-06-2011

Client* : Environmental Pioneers & Solutions Limited Date Received : 08-09-2008

Client Address* : 8/F, Chaiwan Industrial Centre Building, 20 Lee Chung Street, Chaiwan, HK.
 DSD Contract No. DC/2006/11 - Drainage Improvement in Southern Lantau & Construction of

Project* : Mui Wo Village Sewerage Phase 1

Test Location : G/F, 20 Pak Kung Street, Hung Hom, Kowloon. Date Started : 30-05-2011

W.O. No.* : -- Sample Type* : River Water Date Completed : 31-05-2011

GCE Serial No. : WQM052011 GCE Reg. No. : GCE 081096 Test Unit No. : CH 08258

Analysis Description	Test Method	Units	Quality Control Results				
			Method Blank	QC 500 mg/L	QC Duplicate	RPD%	Spike 25 mg/L
Suspended Solids (SS)	APHA 20ed 2540 D	mg/L	< 1.0	497	498	-0.2	27.6
Acceptance Criteria			< 2.5 mg/L	475 ≤ Control Limit ≤ 514		≤ ±5%	21 ≤ R ≤ 29

TEST RESULTS	Sample ID	C1	C1 Duplicate	C2	C2 Duplicate	C3	C3 Duplicate		
	Sampling Date/Time	30 May 2011 / 11:50		30 May 2011 / 12:00		30 May 2011 / 12:10			
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.6	4.4	<1.0	<1.0	12.8	12.4	

TEST RESULTS	Sample ID	M1	M1 Duplicate	M2	M2 Duplicate	M3	M3 Duplicate	M4	M4 Duplicate
	Sampling Date/Time	30 May 2011 / 12:40		30 May 2011 / 12:50		30 May 2011 / 13:00		30 May 2011 / 12:30	
	LOD	Units							
Suspended Solids (SS)	1	mg/L	4.9	5.3	2.5	2.4	8.7	9.1	8.5

* : Information provided by client

Note : This laboratory has no responsibility on sampling and all the test results relate only to the sample tested as received.

Remarks : --

----- End -----

Tested By : C.S. CHAN

Approved Signatory : 

Name : GU CHIN

Checked By : GU CHIN

Post : Chemist

Appendix G
Monitoring Schedule
for May 2011

Environmental Pioneers and Solutions Limited

DC/2006/11 - DRAINAGE IMPROVEMENT IN SOUTHERN LANTAU

Master Schedule of EM&A works in May 2011

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
5/1	5/2	5/3	5/4	5/5	5/6	5/7
		WQM at: 12:37	WQM at: 13:07		WQM at: 14:02 Noise monitoring	
5/8	5/9	5/10	5/11	5/12	5/13	5/14
	WQM at: 15:30		WQM at: 16:15		WQM at: 10:10 Noise monitoring	
5/15	5/16	5/17	5/18	5/19	5/20	5/21
	WQM at: 11:23		WQM at: 12:51		WQM at: 14:25 Noise monitoring	
5/22	5/23	5/24	5/25	5/26	5/27	5/28
	WQM at: 15:45	WQM at: 16:15			WQM & EWQM at: 10:20 Noise monitoring	
5/29	5/30	5/31	6/1	6/2	6/3	6/4
	WQM at: 11:10		WQM at: 12:09			

Noise Monitoring Locations: Total 4 Locations as N1, N2, N3 and N4

Water Quality Monitoring (WQM) Locations: Total 7 Locations as M1, M2, M3, M4, C1, C2 and C3

Appendix H Implementation Status of environmental protection / mitigation measures


Environmental Aspect	Protection / Mitigation Measures	Implementation status	Follow-up action
Air Quality	Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved road, with complete coverage.	Implemented	-
	Use of frequent watering for particular dusty static construction areas and areas close to ASRs.	Implemented	-
	Tarpaulin covering of all dusty vehicle loads transported to and from and between site location;	Deficiency found on 9 Feb 11	-
	Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.	Implemented	-
	Routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.	Implemented	-
Noise	Use of quiet powered mechanical equipment (PME)	Implemented	-
	Adoption of movable noise barriers and temporary noise barriers	Implemented	-
	Application of good site practices mentioned in EM&A manual Clause 3.8.1	Implemented	-
Water Quality	Before commencing any site formation works, all sewer and drainage connections should be sealed to prevent debris, soil, sand etc. from entering public sewers/drains.	Implemented	-
	Temporary ditches should be provided to facilitate run-off discharge into appropriate watercourses, via a silt retention pond. No site run-off should enter the freshwater marshes at Luk Tei Tong.	Implemented	-
	Sand/ silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove sand/ silt particles from runoff to meet the requirements of the Technical Memorandum standard under the Water Pollution Control Ordinance.	Implemented	-
	Water pumped out from foundation excavations should be discharged into silt removal facilities.	Implemented	-
	During rainstorms, exposed slope surface should be covered by a tarpaulin or the means.	Implemented	-
	Exposed soil areas should be minimized to reduce potential for increased siltation and contamination of runoff.	Implemented	-
	Exposed soil surfaces should be protected by paving or fill material as soon as possible to reduce potential of soil erosion.	Implemented	-
	Open stockpiles of construction materials or construction wastes on-site of more than 50m ³ should be covered with tarpaulin or similar fabric during rainstorms.	Implemented	-
	Oils and fuels should only be used and stored on designated areas which have pollution prevention facilities.	Implemented	-
	Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site.	Not available	-
	The excavation and widening works for the drainage improvements to the Pak Ngan Heung River, Tai Tei Tong River, Luk Tei Tong River and Luk Tei Tong By-pass Channel should be carried out in sections (approximately 300–400 m in length) and in dry condition.	Implemented	-

Environmental Aspect	Protection / Mitigation Measures	Implementation status	Follow-up action
	Maintenance desilting of the re-profiled river channels of the Pak Ngan Heung River, Tai Tei Tong River, Luk Tei tong River and Luk Tei Tong By-pass Channel, temporary barrier walls should be used to provide a dry zone for desilting work.	Not applicable at this stage	-
Ecology	Existing natural habitats should be retained as far as practicable	Implemented	-
	Boundary of working areas should be identified to prevent loss of vegetation	Implemented	-
	All existing trees / plant should be well protected within the site or transplanted properly	Implemented	-
	Turf removal from the Luk Tei Tong marsh due to the construction of Luk Tei Tong Bypass Channel shall be minimized	Implemented	-
	Turf from the Luk Tei Tong marsh shall be properly removed, stored, maintained and reused for lining the riverbed of the Luk Tei Tong Bypass Channel	Implemented	-
Chemical and Solid Waste	Chemical wastes should be properly stored in a proper store as per statutory requirements (i.e. on a hard standing, within an enclosed and locked area)	Implemented	-
	Chemical waste stores should be provided with fire precaution facilities (i.e. fire extinguisher, no smoking warning etc).	Implemented	-
	Chemical wastes should be properly stored in corrosion resistant containers placed inside the store and labelled with warning signs in English and Chinese.	Implemented	-
	Chemical wastes should be disposed of by licensed chemical waste collector with supporting delivery records.	Implemented	-
	All containers for fuel, diesel and fluid chemical (in use) and oil filled stationery plants located with proper drip pans.	Implemented	-
	Construction wastes should be managed and disposed to the designated public fill and landfill areas in acceptable manner.	Deficiencies found	
	All waste disposals managed in a proper manner i.e. trip ticket system implementation.	Implemented	-


Appendix I

Graphical plot of water
quality monitoring
results (SS, DO,
turbidity)


Graphical Plot of Turbidity Trend M1&C1(Feb 11 - May 11)

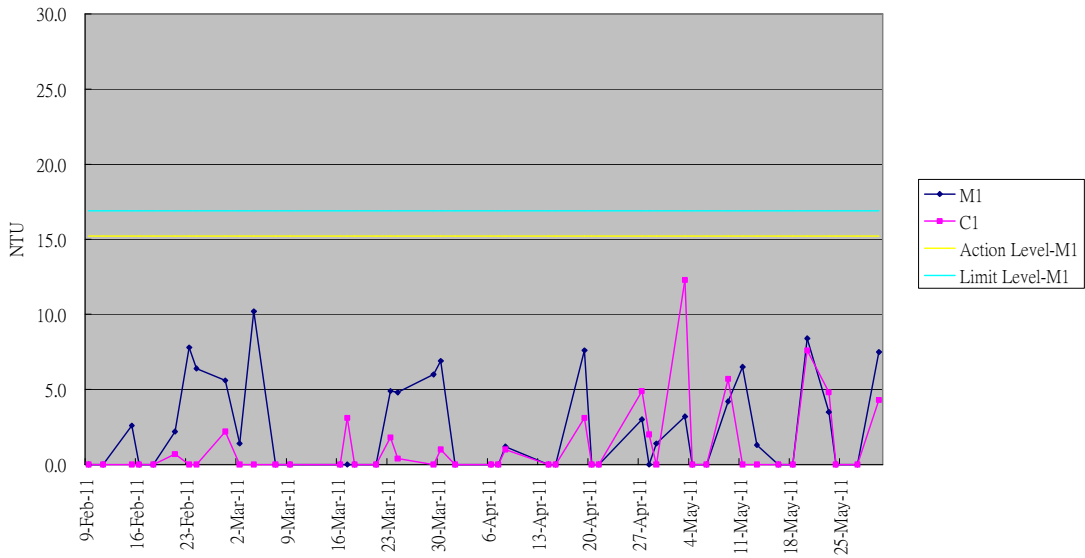


Graphical Plot of Turbidity Trend M2&C2 (Feb 11 - May 11)

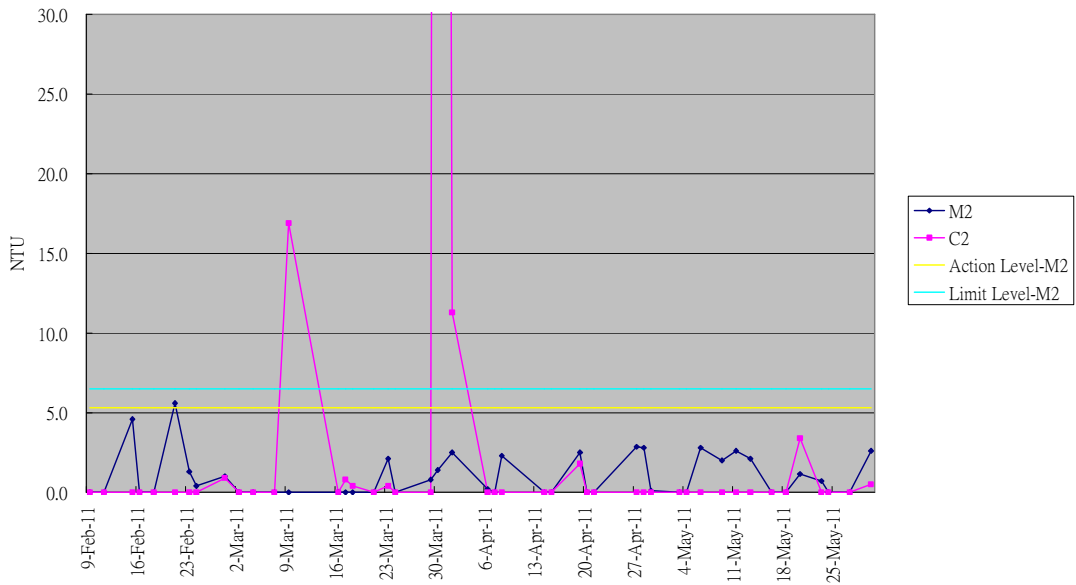


Graphical Plot of Turbidity Trend M3&C3 (Feb 11 - May 11)

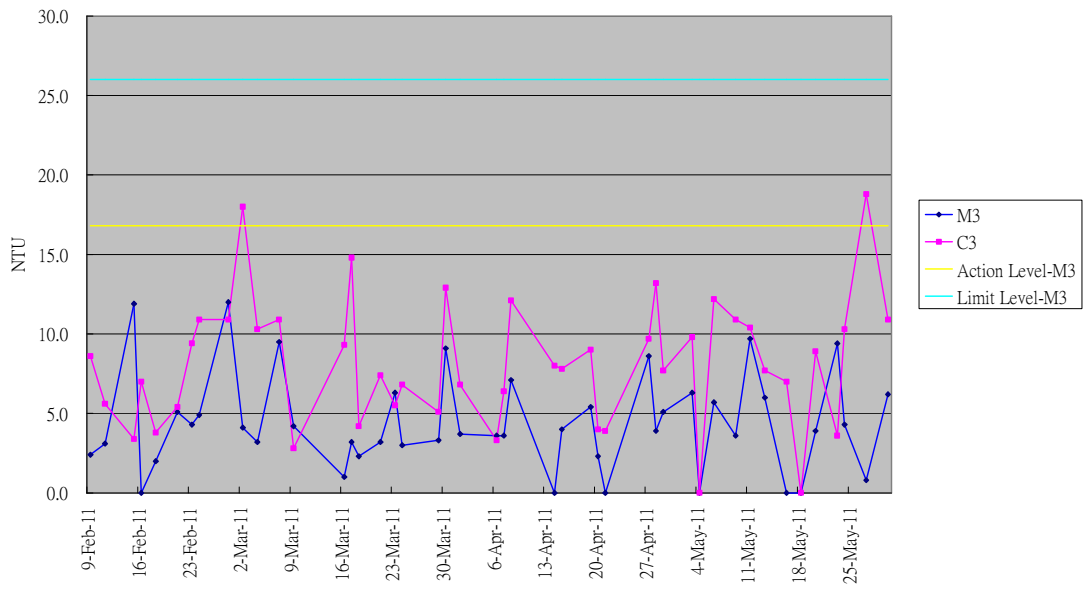


Graphical Plot of Turbidity Trend M4 (Feb 11 - May 11)

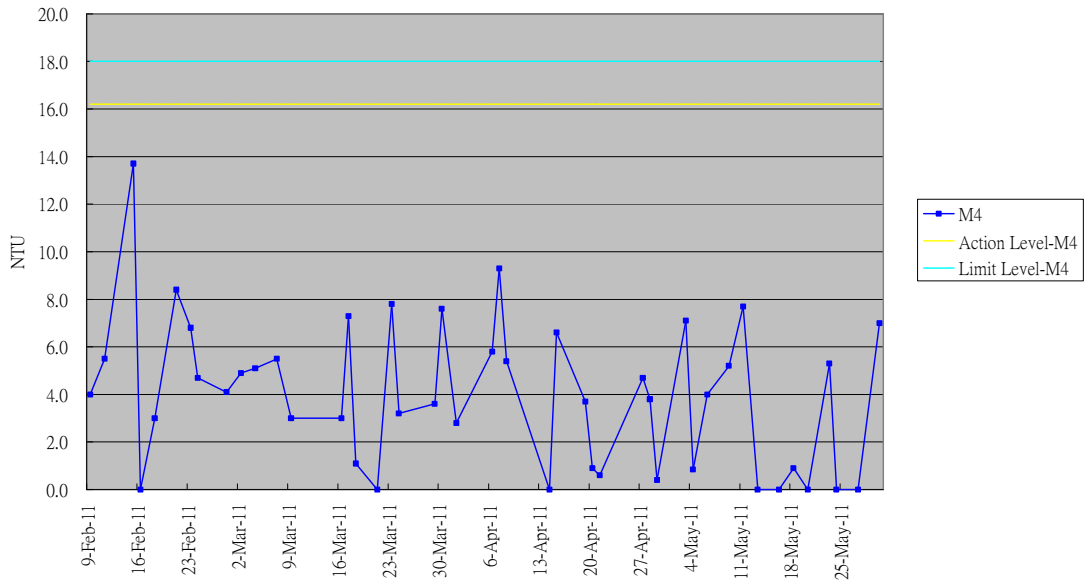


Graphical Plot of Dissolved Oxygen Trend M1&C1 (Feb 11 - May 11)

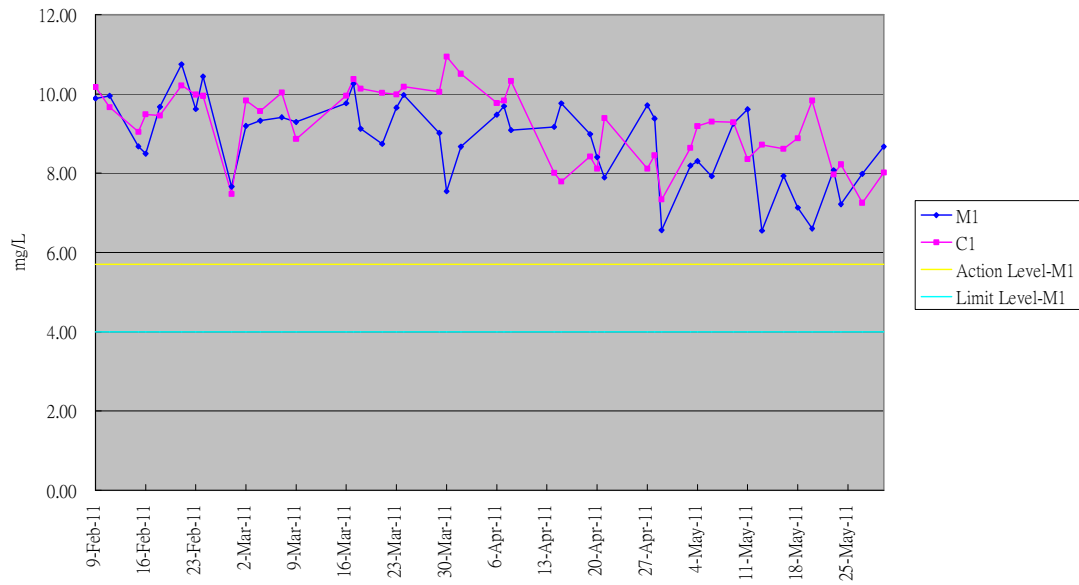


Graphical Plot of Dissolved Oxygen Trend M2&C2 (Jan 10 - Apr 11)

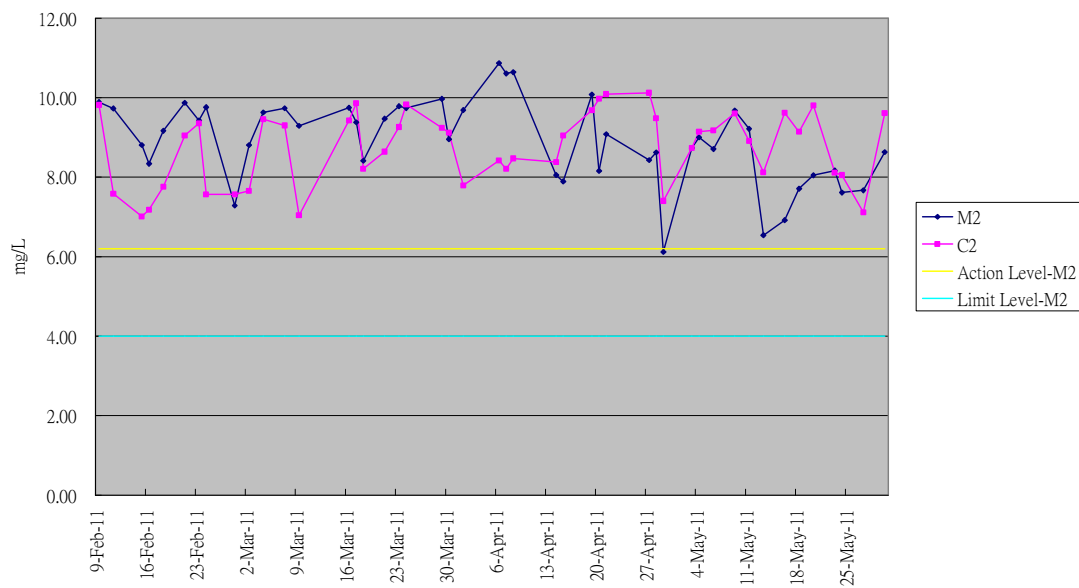


Graphical Plot of Dissolved Oxygen Trend M3&C3 (Feb 11 - May 11)

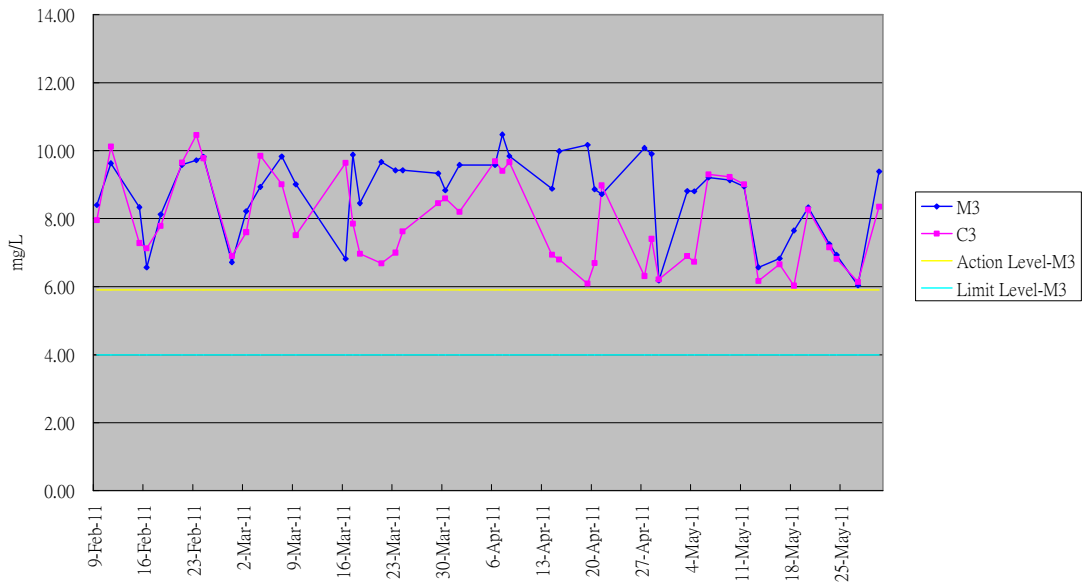


Graphical Plot of Dissolved Oxygen Trend M4 (Feb 11 - May 11)

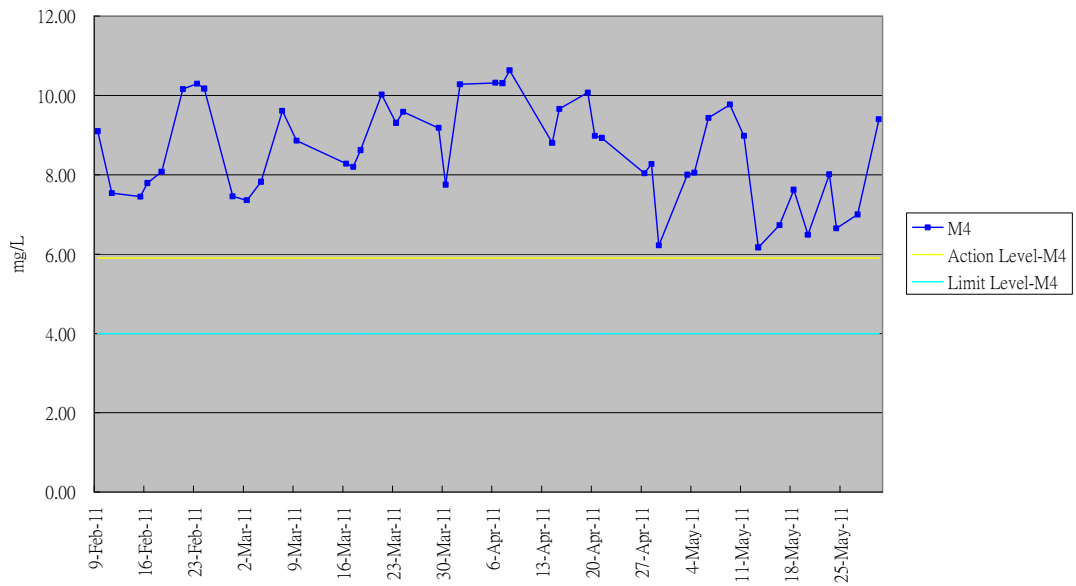


Graphical Plot of Suspended Solid M1&C1 (Feb 11 - May 11)

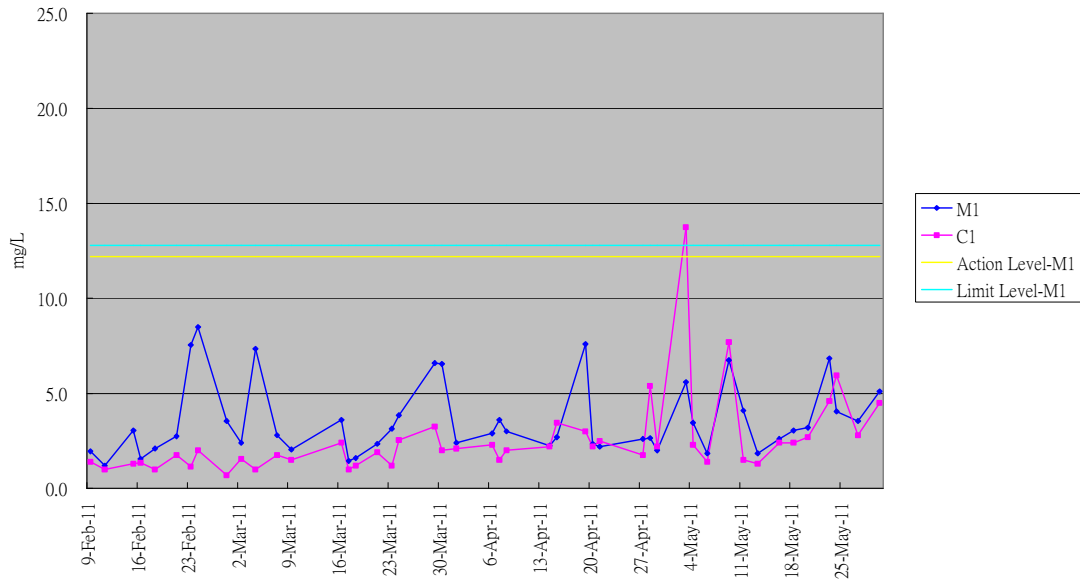


Graphical Plot of Suspended Solid M2&C2 (Feb 11 - May 11)

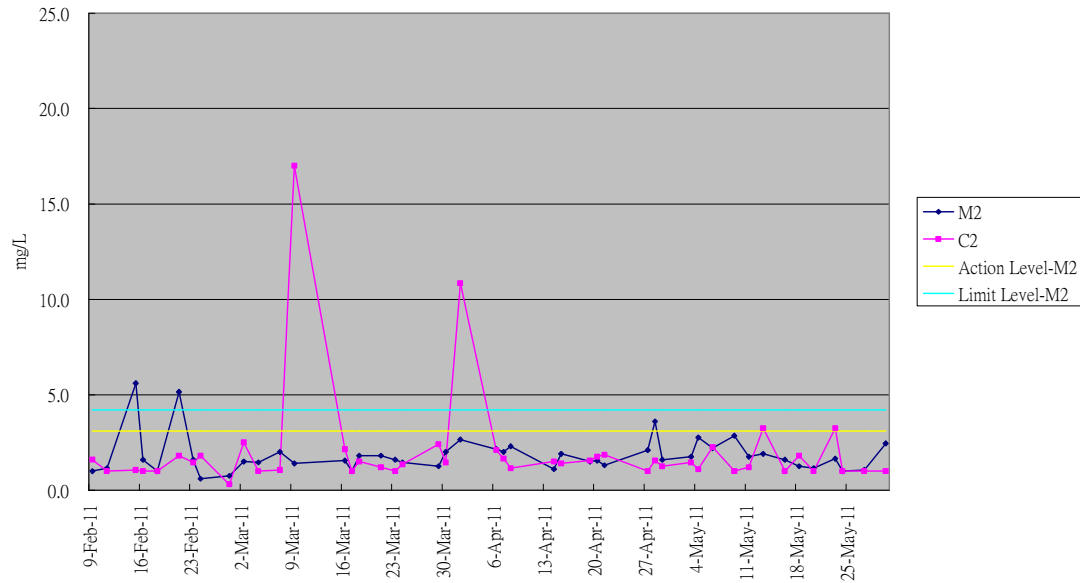

Graphical Plot of Suspended Solid M3&C3 (Feb 11 - May 11)

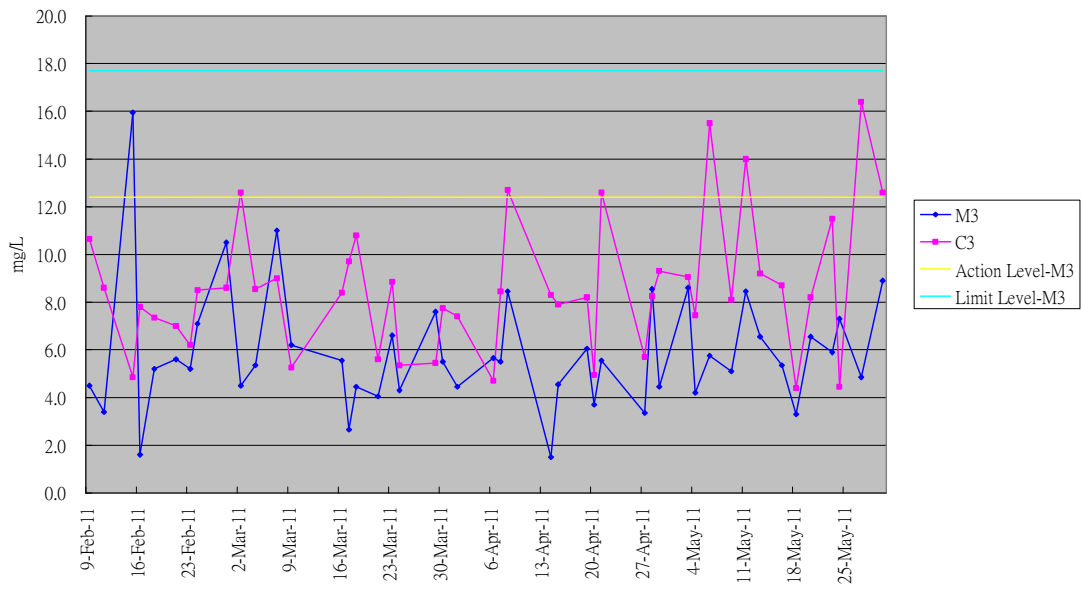

Graphical Plot of Suspended Solid M4 (Feb 11 - May 11)

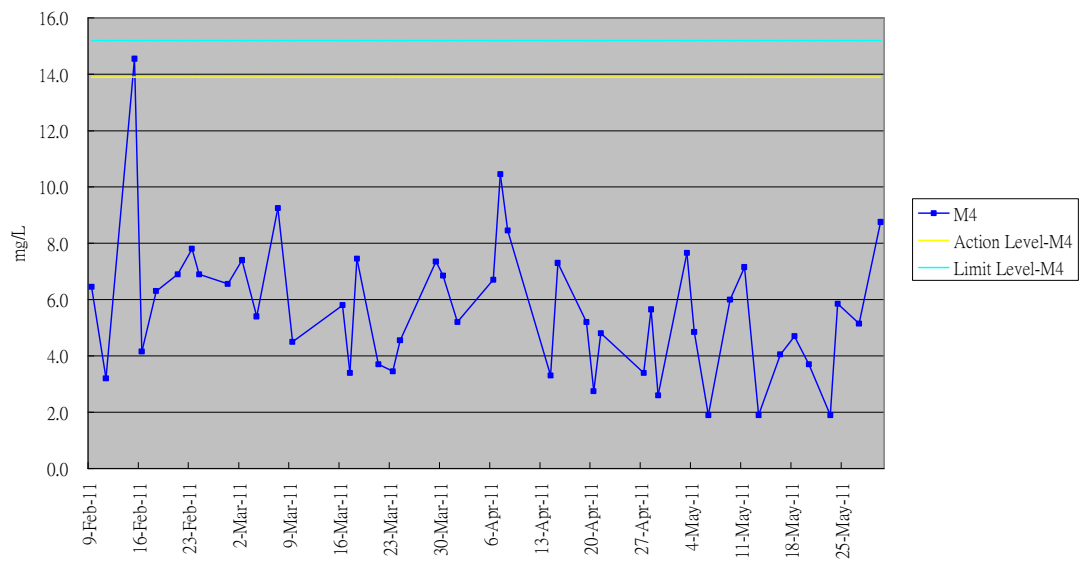

Appendix J

Graphical plot of noise
monitoring results

