


Highways Department

**Agreement No. HMW
5/2009 (EP) Traffic
Improvements to Tuen
Mun Road Town Centre
Section**

Monthly Environmental
Monitoring and Audit
Report - May 2011

Final



Certified by Environmental Team Leader
Coleman Ng
Ove Arup & Partners Hong Kong Ltd



Verified by Independent Environmental Checker
David Yeung
ENVIRON HK Limited

Contents

	Page
Executive Summary	1
1 Environmental Status	3
1.1 Project Background	3
1.2 Construction Programmed	3
1.3 Work Undertaken During the Reporting Month	3
1.4 Project Area, Sensitive Receivers and Environmental Monitoring locations	4
1.5 Impact Monitoring Schedule	5
1.6 Status of Environmental Licensing and Permitting	5
1.7 Purpose of the Report	6
2 Implementation Status	8
2.1 Implementation Status of Mitigation Measures	8
2.2 Updated Implementation Schedule	9
3 Air Monitoring	10
3.1 Air Monitoring Requirements	10
3.2 Air Monitoring Methodology	11
3.3 Monitoring Results and Observations	12
4 Noise Monitoring	13
4.1 Noise Monitoring Requirements	13
4.2 Noise Monitoring Methodology	14
4.3 Monitoring Results and Observations	15
5 Landscape and Visual Monitoring	18
5.1 Landscape and Visual Monitoring Requirements	18
5.2 Audit Results	19
5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures	20
5.4 Recommendations, Corrective Actions and Outstanding Issues	20
6 Waste Disposal	21
7 Environmental Performance	21
7.1 Environmental Site Inspection	21
7.2 Complaint Record	24
7.3 Notification of Summons and Successful Prosecution	25
7.4 Review of Reasons of Non-Compliance	25
8 Future Key Issues	25
8.1 Key Issues for the Coming Month	25
8.2 Environmental Monitoring Program for the Coming Month	25
9 Conclusions and Recommendations	26

9.1	Conclusions	26
9.2	Recommendations	26
10	Reference	26

Appendices

Appendix A

Construction Programme

Appendix B

Environmental Monitoring Programme in the Reporting Month

Appendix C

Implementation Schedule of Mitigation Measures

Appendix D

Calibration Certificates and Spreadsheets of Air Monitoring Equipments

Appendix E

Impact Air Monitoring Results

Appendix F

Wind Data

Appendix G

Calibration Certificates of Noise Monitoring Equipments

Appendix H

Impact Noise Monitoring Results

Appendix I

Landscape Summary Report

Appendix J

Monthly Summary Waste Flow Table

Appendix K

Environmental Monitoring Programme for Coming Month

Appendix L

Complaint Log

Executive Summary

This is the tenth monthly Environmental Monitoring and Audit (EM&A) report prepared by Ove Arup & Partners Hong Kong Limited (Arup), the designated Environmental Team (ET), for the Project "Traffic Improvement to Tuen Mun Road Town Centre Section". This report presents the results of EM&A works conducted in the month of May 2011 (1 to 31 May 2011).

In the reporting month, the following activities took place for the Project:

- Site clearance
- Site hoarding construction;
- Tree felling and transplanting;
- Temporary footbridge construction;
- Pilling works;
- Ground investigation; and
- Underground utilities and drainage diversion.

Monitoring of 24-hour Total Suspended Particulates (TSP) and noise during non-restricted hours was performed and the results were checked and reviewed. Site audits were conducted on weekly basis. The implementation of the environmental mitigation measures, Event and Action Plans were checked.

Impact monitoring was carried out at 6 air quality sensitive receiver (SR) and 6 noise SRs during the reporting month.

Environmental Monitoring Works – Breaches of Action and Limit Levels

Air Quality

All measured 24-hour TSP concentrations in the reporting month were below the Action and Limit (AL) Levels.

Noise

Totally nine limit level exceedances for noise measurements during non-restricted hours were recorded in the reporting month. Based on the field observations, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor.

No Action Level exceedance of construction noise was recorded in the reporting month.

Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor. No non-compliance was recorded.

Landscape and Visual Audit

In the reporting month, landscape and visual site audit in accordance with the requirements stipulated in the EIA report was conducted on 5 and 26 May 2011.

In the reporting month, total 478 trees were felled and the pruning of the transplanted trees was carried out in accordance with the Specification for Tree Protection and Transplanting Works in Landscape Plan. The updated statuses of the felled and transplanted trees during the reporting month are described in Section 5.

The implementation and maintenance of landscape and visual mitigation measures, listed in EIA report, were checked during the site audit. No substantial change of LR, LCA and VSR was noted. No non-compliance has been triggered during the reporting month.

Waste Disposal

Inert C&D materials with actual amount of 2,968.875 m³ were generated and disposed of at public fills at Tuen Mun Area 38 in the reporting month. 53.625 m³ general refuse were generated and disposed of at WENT landfill in the reporting month.

Environmental Licensing and Permitting

Permits or licenses granted to the Project included the Environmental Permit of the Project (EP-342/2009/B), Chemical Waste Producer Registration (5213-324-G3597-01) and Construction Waste Billing Account (7010350);

8 numbers of Construction Noise Permits and 2 numbers of Wastewater Discharge License under WPCO (WT00007251-2010 and WT00008195-2011).

Environmental Auditing

A total of 4 environmental site audits were conducted on a weekly basis in the reporting month. No non-conformance to the environmental requirements was identified during the reporting month.

Complaint Log

One environmental complaint regarding the cleaning water spillage to TMR was recorded in the reporting month. After the investigations, it is concluded that the complaint was attributable to the Contractor. The corresponding mitigation measure due to the complaint was recommended to be carried out by the Contractor.

Notifications of Summons and Successful Prosecutions

No summonses or prosecution related to the environmental issues were made against the Project in the reporting month.

Reporting Changes

There were no reporting changes in the reporting month.

Future Key Issues

Construction noise is one of the key environmental issues. The implemented construction noise mitigation measures should also be maintained and improved as necessary. Especially in restricted hours, the conditions stipulated in CNPs should be strictly followed when the construction works were carried out during the restricted hours.

Construction dust is another key environmental issue. The implemented construction dust mitigation measures should also be maintained and improved as necessary. Furthermore, water quality impact is also key environmental issue. As rainy season has approached, special attention should be paid to avoid any muddy surface runoff from exposed soil surface during rainy days. The effective and efficiency mitigation measures should be strictly implemented and improved if necessary.

1 Environmental Status

1.1 Project Background

Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the Environmental Team (ET) for *Agreement No. CE22/2005 (HY) Supplementary Agreement 1 Traffic Improvements to Tuen Mun Road Town Centre Section* (the Project) under Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section. Environmental parameters including air quality, noise and landscape and visual are required for baseline monitoring prior to the commencement of the Project. The Project was commenced on August 2010 and to be completed on January 2014.

The Project involves widening the following sections of TMR from dual-two carriageway to dual-three carriageway:

- Wong Chu Road Section, (from Wong Chu Road Interchange to Tuen Hing Road);
- Tuen Mun Town Plaza Section, (from Yan Oi Town Square to Tuen Hing Road).

The Project is a designated project under Schedule 2 of the Environmental Impact Assessment (EIA) Ordinance (Cap. 499). Environmental Monitoring and Audit (EM&A) work is required in accordance with the conditions stipulated in the Environmental Permit (EP) (EP-342/2009/A) and the EM&A Manual of the Project.

1.2 Construction Programme

An up-to-date rolling construction programme is attached in **Appendix A**.

1.3 Work Undertaken During the Reporting Month

The major construction activities carried out by the Contractor in the reporting month are summarized in **Table 1.1**. Location of the works area is indicated in **Figure 1.1**. The structure of the project organisation in relation to the environmental management is shown in **Figure 1.2**. Contacts of key environmental staff of the Project and are shown in **Table 1.2**.

Table 1.1 Construction activities in the reporting month

Locations	Major Works Undertaken
All area	Site clearance, site hoarding construction, tree felling and transplanting, ground investigation, temporary footbridge construction; pilling works, underground utilities and drainage diversion

Figure 1.1 Site plan of the Project

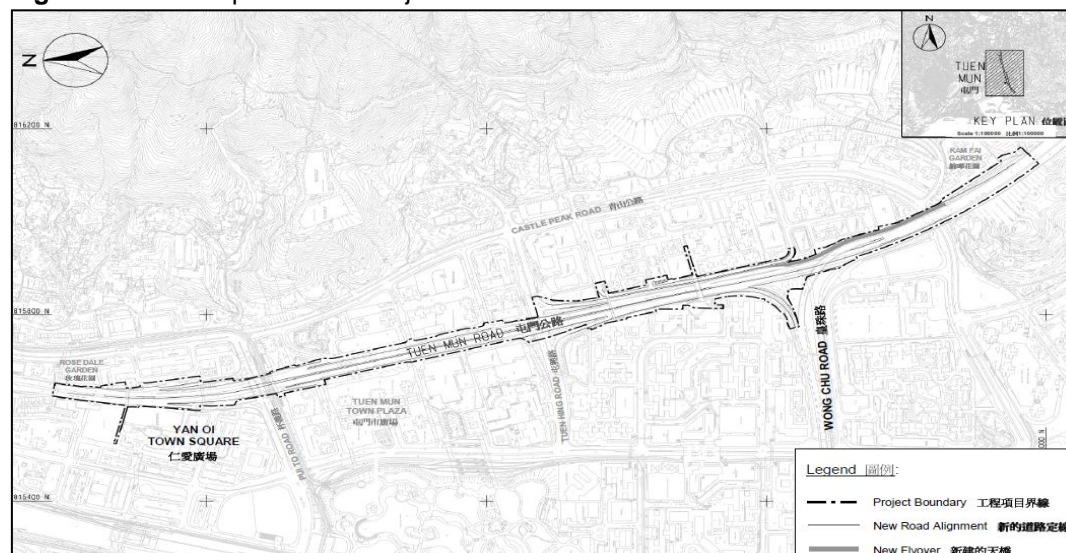
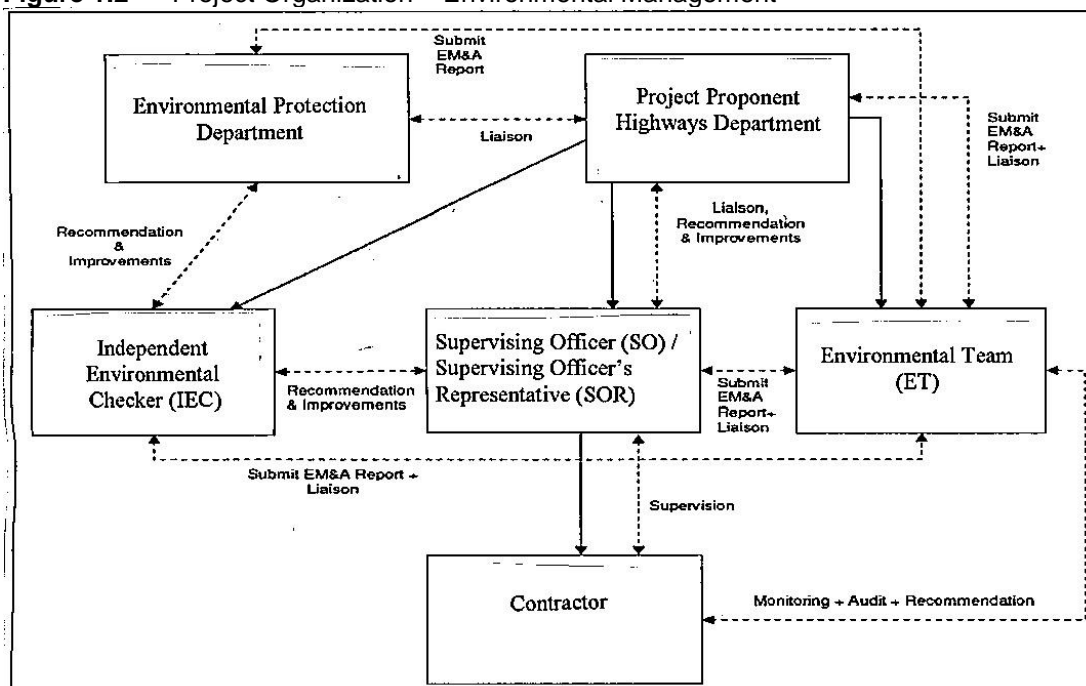


Figure 1.2 Project Organization – Environmental Management**Table 1.2** Contacts of key environmental staff

Organization	Name	Telephone
Environmental Protection Department		
Environmental Protection Officer (Strategic Assessment)22	Thomas To	2835 1103
Project Proponent		
Highways Department: Senior Engineer	Kenneth Chan	2762 3422
Supervising Officer / Supervising Officer's Representative		
AECOM Asia Co. Ltd.: Chief Resident Engineer	Patrick Lee	2969 9200
Independent Environmental Checker		
ENVIRON Hong Kong Limited: Independent Environmental Checker	David Yeung	3743 0717
Environmental Team		
Ove Arup & Partners Hong Kong Ltd: Environmental Team Leader	Coleman Ng	2268 3097
Contractor		
China Harbour Engineering Company Limited		
Site Agent	W.S. Ng	2403 0529
Environmental Officer	Marko Chan	2403 0527

1.4 Project Area, Sensitive Receivers and Environmental Monitoring locations

The Project area is shown in **Figure 1.1**, while **Table 1.3** and **Figure1.3** show the names and locations of the sensitive receivers and monitoring stations.

Table 1.3 Summary of air and noise monitoring stations

ID	Premise
Air	
AM1	Chung Sing Benevolent Society Mrs. Aw Boon Haw Secondary School

ID	Premise
AM2	Tung Wah Group of Hospitals Tai Tung Pui Social Service Building
AM3	Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School
AM4	The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School
AM5	Tuen Mun Town Hall
AM6	Yan Oi Tong Jockey Club Community and Sports Centre
Noise	
N1	Kam Fai Garden
N2	Tung Wah Group of Hospitals Tai Tung Pui Social Service Building
N3	Po Leung Kuk The Hong Kong Taoist Association Yuen Yuen Primary School
N4	Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School
N5	Tuen King Building
N6	The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School

1.5 Impact Monitoring Schedule

Environmental monitoring and audit will be carried out in accordance with the requirements stipulated in the EM&A manual. Air, noise, landscape and visual monitoring as well as weekly site audit schedule for the reporting month with respect to the construction programme is shown in **Appendix B**.

1.6 Status of Environmental Licensing and Permitting

All permits/licences inspected in the reporting month are summarised in **Table 1.4**. They are all properly kept by the contactor at their site office.


Table 1.4 Summary of environmental licensing status

Types of Permits / Licenses	Reference No.	Valid from	Valid to
Environmental Permit	EP-342/2009	15 May 09	Superseded
	EP-342/2009/A	27 Oct 09	Superseded
	EP-342/2009/B	14 Feb 11	N/A
Discharge License under WPCO	WT00007251-2010	12 Aug 10	31 Aug 15
	WT00008195-2011	06 Jan 11	30 Sep 15
Notification of Construction Work under APCO	Ref.: 314528	25 Feb 2010	N/A
Construction Noise Permit	GW-RW0589-10	24 Nov 10	21 May 11
	GW-RW0640-10	01 Dec 10	22 May 11
	PP-RW0022-10	23 Feb 11	31 May 11
	GW-RW0052-11	12 Feb 11	07 Aug 11
	GW-RW0164-11	12 Mar 11	12 Jun 11
	GW-RW0228-11	03 Apr 11	26 Jun 11
	GW-RW0353-11	24 May 11	23 Nov 11
	GW-RW0358-11	24 May 11	19 Nov 11
Chemical Waste Producer	5213-424-C3597-01	26 Mar 10	N/A

Registration			
Construction Waste Billing Account	7010350	25 Mar 10	N/A

1.7 Purpose of the Report

The purpose of the monthly EM&A report is to provide the information on monitoring methodology, monitoring results, environmental permit status, site audit findings, recommendations and conclusions for the scope of impact EM&A. This is the tenth monthly EM&A report summarising the monitoring methodology, locations, periods, frequencies, results and any observation from the air quality, noise, water quality, ecology, waste management, landscape and visual monitoring and environmental site audit from 1 to 31 May 2011.

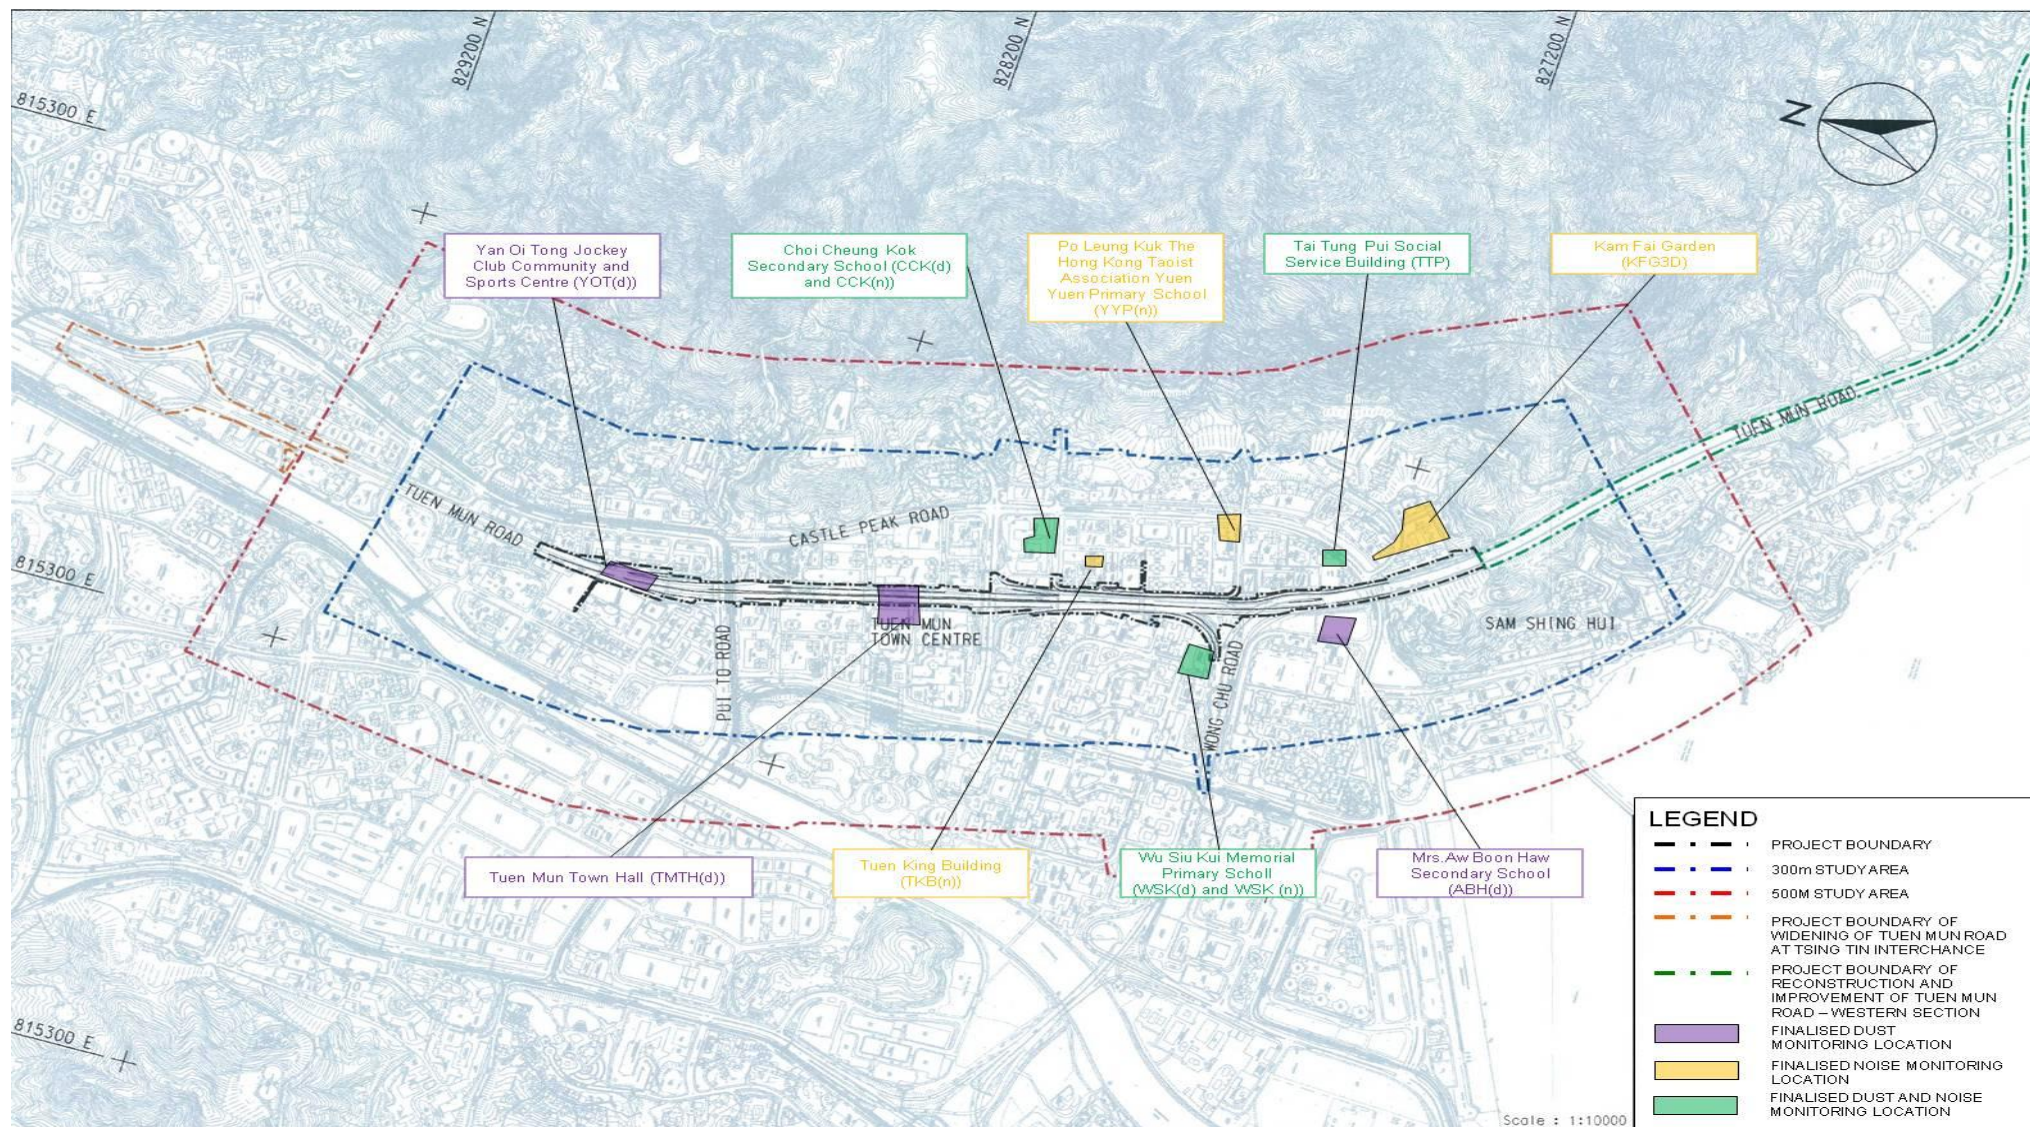Figure 1.3 Location of air and noise monitoring stations

2 Implementation Status

2.1 Implementation Status of Mitigation Measures

During weekly site inspections, the environmental protection, and pollution control/mitigation measures in accordance with the requirements stipulated in the EIA were observed. **Table 2.1** summarises the key observations and ET's corresponding recommendations while the Contractor's response and follow-up status are described in Section 7.1.

Table 2.1 Summary of the key observations and ET's recommendations

Location	Key Observations and Recommendations
Air Quality Mitigation Measures	
Yan Oi Tong Street	Excessive emission from a mobile crane was observed, the Contractor was reminded to carry out proper maintenance.
Yan Oi Tong Street and Tuen Hing Road	The Contractor was reminded to minimize the gaps between cover sheets of the cement store.
Rosedale Garden and Tuen Hing Road	The Contractor was reminded to increase the water spray frequency for minimise dust impact.
Tuen Fat Road	Dark smoke emission generator was observed. The Contractor should inspect the machine maintenance and fix it as soon as possible.
Tuen Hi Road	Dark smoke emission from pilling machine was observed. The Contractor should enhance the machine maintenance and fix it as soon as possible.
Water Quality Mitigation Measures	
Yan Ching Street	Stagnant water within the site area should be removed as soon as possible to avoid mosquito breeding.
Yan Chin Bridge/Yan Oi Tong Street	The contractor was reminded to desilt the U-Channel along TMR.
All area	The Contractor was reminded to carry out proper temporary drainage control to comply with WPCO requirements.
Yan Ching Street (near Yan Oi Tong Circuit); & Area under Wong Chu Road Flyover	The Contractor should enhance the cleaning frequency of the U-Channel to avoid any silt/sand accumulation.
Tuen Fat Road	The Contractor was reminded to extend the sand bags bunding along the site bounding (Tuen Fat Road) and enhance the inspection to avoid any surface runoff overflowing to public area.
Waste Management	
Yan Oi Tong Circuit	The waste cement bags should be removed regularly to avoid accumulation. Tarpaulin covering should be provided before disposal to avoid dust disturbance.
Pui To Road	Drip tray should be provided for the chemicals placing.
Tsing Hoi Circuit	The stockpiles should not be placed too close to the TMR without barrier/bunding to avoid the loose soil dropping to TMR.
	Accumulated debris and construction waste should be removed regularly to avoid accumulation.
Rosedale Garden	The drip tray of air compressor (no.62) contained oil-bearing wastewater. The Contractor was reminded to remove it as chemical waste.
	Oil leakage was observed at a Boring Machine (TMT-113). The Contractor was reminded to remove the contaminated soil as chemical waste and carry out

Location	Key Observations and Recommendations
	proper maintenance of the machine.
Tuen Hing Road	The Contractor was reminded to dispose of the rubbish (at site entrance) as soon as possible.
Yan Oi Tong Street	The Contractor was reminded to place the sands bags at both ends of site entrance (including Rosedale Garden)
Tuen Hi Road	The Contractor should enhance the inspection of sandbags condition and replace the damaged sandbags as soon as possible. In addition, the Contractor was reminded to provide additional bunding between pilling areas and haul road.
General	
Entire site area	The Contractor was reminded to update the new version Environmental Permit as soon as possible and display on the Project site entrance/exits.

2.2 Updated Implementation Schedule

According to the Environmental Permit, the mitigation measures detailed in the permits are required to be implemented. The Implementation Schedule of Mitigation Measures was inspected during the weekly site inspections in reporting month. The details of the findings/observations are described in Section 7.1. An updated summary of the Implementation Schedule of Mitigation Measures is presented in **Appendix C**.

3 Air Monitoring

3.1 Air Monitoring Requirements

Monitoring Parameters

Air quality monitoring shall be measured in terms of the TSP levels for 1-hour and 24-hour period.

Monitoring Frequency

24-hour TSP levels shall be monitored during the construction stage while 1-hour TSP levels shall be required to monitor in case of complaints received. The monitoring parameters and frequency are summarised in **Table 3.1**.

Table 3.1 TSP monitoring parameters and frequency

Parameters	Monitoring Frequency
24-hour TSP	Once every 6 days
1-hour TSP	3 times every 6 days (as required in case of complaints)

Monitoring Locations

In accordance with the EM&A Manual and the subsequent Baseline Report, six air quality monitoring locations during construction stage are required, namely:

- (i) Chung Sing Benevolent Society Mrs. Aw Boon Haw Secondary School (AM1);
- (ii) Tung Wah Group of Hospitals Tai Tung Pui Social Service Building (AM2);
- (iii) Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School (AM3);
- (iv) The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School (AM4);
- (v) Tuen Mun Town Hall (AM5); and
- (vi) Yan Oi Tong Jockey Club Community and Sports Centre (AM6).

Wind Monitoring

Wind monitoring data including wind speed and wind directions shall be collected from Hong Kong Observatory – Tuen Mun Monitoring Station.

Environmental /Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 3.2 and 3.3**.

Table 3.2 Action and Limit Level for air quality monitoring of 1-hour TSP level

Level	Air Monitoring Stations					
	AM1	AM2	AM3	AM4	AM5	AM6
Action Level, $\mu\text{g}/\text{m}^3$	290	291	287	292	286	290
Limit Level, $\mu\text{g}/\text{m}^3$	500					

Notes:

1-hr TSP monitoring would be required in case of receiving complaints.

Table 3.3 Action and Limit Level for air quality monitoring of 24-hour TSP level

Level	Air Monitoring Stations ^(Note 1)					
	AM1	AM2	AM3	AM4	AM5	AM6
Action Level, $\mu\text{g}/\text{m}^3$	146	151	150	150	146	147
Limit Level, $\mu\text{g}/\text{m}^3$	260					

3.2 Air Monitoring Methodology

3.2.1 Monitoring Equipment

High Volume Sampler (HVS) was used to monitor the 24-hour TSP. **Table 3.4** shows the equipment used for the air quality monitoring.

Table 3.4 Air quality equipment list for impact air quality monitoring

Equipment	Manufacturer & Model No	Measurement Parameter	Quantity	Serial No.
High Volume Sampler	GS-2310105 / TE-5170	24-hour TSP	6	521, 522, 505, 1278, 516 & 510
Fibreglass Filter	G810		30	-
HVS Calibration Kit	GMW-2535		1	1378

3.2.2 Maintenance and Calibration

The HVSs and their accessories were frequently checked and maintained in accordance with the manufacturer's operation and maintenance manual. The maintenance included checking of supporting screen and gasket, as well as routine replacement of motor carbon brushes for the blower motor. The power cords and power supply were checked each time before sampling to ensure proper operation.

The HVSs were calibrated at 2-month intervals using GMW-2535 calibration kit which is re-calibrated by the manufacturer after one year of use. The calibration spreadsheets of the HVS and calibration certificate of the calibration kit are provided in **Appendix D**.

3.2.3 Monitoring Procedures

Specifications of the HVS are as follows:

- 0.6 – 1.7 m³/min (20 – 60SCFM);
- Equipped with a timing/control device with +/- 5 minutes accuracy for 24 hour operation;
- Installed with elapsed time meter with +/- 2 minutes accuracy for 24 hour operation;
- Capable of providing a minimum exposed area of 406 cm² (63in²);
- Flow control accuracy: +/-2.5% deviation over 24-hour sampling period;
- Equipped with a shelter to protect the filter and sampler;
- Incorporated with an electronic mass flow rate controller or other equivalent devices;
- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easy to change the filter; and
- Capable of operating continuously for 24-hour period.

The HVSs were equipped with an electronic mass flow controller and calibrated against a traceable standard at regular intervals. All equipment, calibration kit and filter papers were clearly labelled.

The relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and other special phenomena observed and work progress of the concerned site were recorded.

A HOKLAS accredited laboratory (ALS Technichem (HK) Pty Ltd (HOKLAS no.: 066)), in accordance with their standard QA/QC procedures, with constant temperature and humidity

control as well as equipped with necessary measuring and conditioning instruments to handle the 24-hour TSP samples was employed for sample analysis, and equipment calibration and maintenance. Filter papers of size 8"x10" were labelled before sampling. They were inspected clean with no pin holes and conditioned in a humidity controlled chamber for over 24-hour and be pre-weighed before use for the sampling.

The 24-hour TSP levels were measured by following the standard High Volume Method for Total Suspended Particulates as set out in the *Title 40 of the United States Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. TSP was sampled by drawing air through a conditioned, pre-weighed filter paper inside the HVS at a controlled air flow rate. After 24-hour sampling, the filter papers loaded with dust were kept in a clean and tightly sealed plastic bag, and then returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with a readout down to 0.1 mg. All the collected samples shall be kept in a good condition for 6 months before disposal.

3.3 Monitoring Results and Observations

3.3.1 Weather Condition

No adverse weather conditions were recorded during the monitoring dates.

3.3.2 Air Quality Monitoring Results

Monitoring of 24-hour TSP was conducted on 5, 11, 17, 23 and 28 May 2011. All monitoring data and graphical presentation of the monitoring results are provided in **Appendix E** and are summarised in **Table 3.5**. The graphical presentations of the monitoring results are provided in **Appendix E**. Wind data obtained from the Hong Kong Observatory – Tuen Mun station during the reporting period is presented in **Appendix F**.

Table 3.5 Summary of impact air quality monitoring results for reporting month

	Location					
	AM1	AM2	AM3	AM4	AM5	AM6
Average 24-hr TSP Concentration, $\mu\text{g}/\text{m}^3$ (Range)	34 (22 – 56)	41 (18 – 71)	48 (26 – 77)	41 (26 – 68)	27 (14 – 41)	30 (17 – 36)

All 24-hour TSP measurements during the reporting month were below the Action/Limit Level. No exceedance of action and limit level was found.

3.3.1 General Observations

Major construction works including site clearance, site hoarding construction, pilling works, ground investigation and underground utilities diversion were implemented during the reporting month. No abnormal condition was recorded during monitoring period.

4 Noise Monitoring

4.1 Noise Monitoring Requirements

Monitoring Parameters

Construction noise shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{10} and L_{90} shall also be recorded as supplementary reference information for data auditing.

Monitoring Frequency

Noise measurements shall be conducted on a weekly basis. The monitoring time periods, monitoring parameters and frequency are summarised in **Table 4.1**.

Table 4.1 Construction noise monitoring parameters and frequency

Time Period (when construction activity is found)	Parameters	Monitoring Frequency
Between 0700-1900 hours on normal weekdays	L _{eq} (30 min)	Once per week
Between 1900-2300 hours on normal weekdays	L _{eq} (5 min)*	
Between 2300-0700 hours of next day		
Between 0700-1900 hours on holidays		

* The $L_{eq(5 \text{ min})}$ will only be measured if construction activities are conducted.

Monitoring Location

In accordance with the EM&A Manual and the subsequent Baseline Report, six noise monitoring location during construction stage is required, namely:

- (i) Kam Fai Garden (N1);
- (ii) Tung Wah Group of Hospitals Tai Tung Pui Social Service Building (N2);
- (iii) Po Leung Kuk The Hong Kong Taoist Association Yuen Yuen Primary School (N3);
- (iv) Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School (N4);
- (v) Tuen King Building (N5); and
- (vi) The Chinese Manufacturers' Association of Hong Kong Choi Cheung Kok Secondary School (N6).

Environmental /Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 4.2**.

Table 4.2 Action and Limit Levels of construction noise

Location ^(Note 1)	Time Period	Action Level	Limit Level dB(A) ^(Note 2)
N1, N2 & N5	0700 - 1900 hours on normal weekdays	When one documented complaint is received	75
	0700 - 2300 hours on holiday; and 1900 – 2300 hours on all other days		-
	2300 – 0700 hours of next day		-
N3, N4 & N6	0700 - 1900 hours on normal weekdays	When one documented complaint is received	70/65 (Note 3)
	0700 - 2300 hours on holiday; and 1900 – 2300 hours on all other days		-
	2300 – 0700 hours of next day		-

Notes:

1. The detail of monitoring locations was presented in Table 2.2.
2. For normal day-time working hours, the noise criteria are 70 dB(A) and 65 dB(A) for normal reaching periods and examination period

respectively.

3. If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be follows.

4.2 Noise Monitoring Methodology

4.2.1 Monitoring Equipment

Noise level was measured by a Sound Level Meter (SLM) in terms of A-weighted equivalent continuous sound pressure level. L_{eq} , L_{10} and L_{90} were recorded as supplementary information for data auditing. **Table 4.3** shows the equipment list of the noise monitoring.

Table 4.3 Noise equipment list for impact noise monitoring

Equipment	Manufacturer & Model No.	Serial No.	Precision Grade	Qty.
Integrated SLM	Brüel & Kjær 2238	2320694, 2320696, 2320707, 2562763, 2654435 & 2654436	IEC 651 Type 1 IEC 804 Type 1	6
½" free-field microphone	Brüel & Kjær 4188	2641132, 2630747, 2630746, 2658559, 2658546 & 2658547		6
Windshield	Brüel & Kjær UA0237	--		6
Sound level calibrator	Rion NC-74	34304660	IEC 942 Type 1	1

4.2.2 Maintenance and Calibration

The SLM and calibrator in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specifications according to the EM&A manual.

SLM complying with the standards of IEC 651 (Fast, Slow, Impulse rms detector tests) and IEC 804 (L_{eq} functions) and acoustical calibrator complying with IEC 942 were adopted for the noise measurement. All equipments are calibrated annually in-house using Brüel & Kjær (B&K) calibrator model no 4226. The 4226 calibrator is annually calibrated under the accreditation of United Kingdom Accreditation Service. The in-house calibration that has been undertaken can be traced back to the National Physical Laboratory. The calibration certificates for the noise equipment are given in **Appendix G**.

4.2.3 Monitoring Procedures

- The SLM and battery were checked to ensure that they are in proper condition. The SLM was set on a tripod at 1.2m above ground and at least 1m from the exterior of the building façade;
- Before conducting the measurement, the SLM was calibrated by an acoustical calibrator;
- Measurement parameter was set to A-weighted sound pressure level. The time weighting was set in fast response and the time period of measurement at 30 minutes;
- Wind speed was checked during noise monitoring to ensure the steady wind speed does not exceed 5m/s, or wind with gusts does not exceed 10m/s;
- Any abnormal conditions that generated intrusive noise during the measurement was recorded on the field record sheet;
- After each measurement, the equivalent continuous sound pressure level (L_{eq}), L_{10} and L_{90} were recorded on the field record sheet;
- After conducting the measurement, the SLM was calibrated by an sound level calibrator; and

- The SLM was re-calibrated by the sound level calibrator to confirm that there is no significant drift of reading. Measurements shall be accepted as valid only if the calibration levels before and after the noise measurement agrees to within 1.0 dB.

4.3 Monitoring Results and Observations

4.3.1 Weather Condition

The weather condition was mainly sunny during the noise monitoring period in the reporting month.

4.3.2 Noise Monitoring Results

Monitoring of the construction noise level was conducted during non-restricted hours on 6, 12, 18 and 24 May 2011 at monitoring locations N1, N2, N3, N4, N5 and N6. All monitoring data and graphical presentation of the monitoring results are provided in **Appendix H** and are summarised in **Table 4.4 to 4.9**. The graphical presentations of the monitoring results are provided in **Appendix H**.

Table 4.4 Summary of impact noise monitoring at location N1 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
6 May 11	09:50-10:20	75	76	Measured ≤ Baseline	75
12 May 11	09:35-10:05	78		73	
18 May 11	09:40-10:20	77		68	
24 May 11	09:50-10:20	74		Measured ≤ Baseline	

Notes:

- Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.5 Summary of impact noise monitoring at location N2 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
6 May 11	10:35-11:05	76	78	Measured ≤ Baseline	75
12 May 11	10:30-11:00	78		Measured ≤ Baseline	
18 May 11	10:30-11:00	76		Measured ≤ Baseline	
24 May 11	10:30-11:00	76		Measured ≤ Baseline	

Notes:

- Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.6 Summary of impact noise monitoring at location N3 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
6 May 11	11:20-11:50	69	69	Measured ≤ Baseline	70
12 May 11	11:15-11:45	68		Measured ≤ Baseline	
18 May 11	11:10-11:40	68		Measured ≤ Baseline	
24 May 11	11:05-11:35	67		Measured ≤ Baseline	

Notes:

1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.**Table 4.7** Summary of impact noise monitoring at location N4 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
6 May 11	08:30-09:00	67	67	Measured ≤ Baseline	70
12 May 11	08:30-09:00	67		Measured ≤ Baseline	
18 May 11	08:30-09:00	66		Measured ≤ Baseline	
24 May 11	11:30-12:00	64		Measured ≤ Baseline	

Notes:1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.**Table 4.8** Summary of impact noise monitoring at location N5 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
6 May 11	13:00-13:30	72	70	68	75
12 May 11	13:00-13:30	71		65	
18 May 11	13:00-13:30	72		66	
24 May 11	13:10-13:40	72		66	

Notes:1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.**Table 4.9** Summary of impact noise monitoring at location N6 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
6 May 11	14:00-14:30	71	69	66	70
12 May 11	13:50-14:20	71		64	
18 May 11	13:45-14:15	71		65	
24 May 11	13:45-14:15	70		62	

Notes:1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.**Restricted Hours**

In the reporting months, the construction works and activities such as mobilization of materials and plants etc were carried out during restricted hours. The granted Construction Noise Permits (CNPs) were issued by EPD for the related activities before the works commencement, the Contractor strictly followed the conditions stipulated in the CNPs. There was no non-compliance recorded during the reporting month.

4.3.3 Exceedance of Limit and Action Levels for Construction Noise

Totally nine limit level exceedances for noise measurements during non-restricted hours were recorded in the reporting month and are summarized in **Table 4.10**.

Table 4.10 Summary of exceedance of Limit Level for construction noise in the reporting month

Location	No. of exceedance of Limit Level	Date of exceedance
N1	2	12 and 18 May 2011
N2	4	6, 12, 18 and 24 May 2011
N6	3	6, 12 and 18 May 2011

Based on the field observations, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor. No Action Level exceedance was recorded in the reporting month.

Baseline noise level were retrieved and shown in **Table 4.4 to 4.9**. Comparison is made between the monitoring results against the baseline noise level, the monitoring results were lower to the baseline level. Based on the on-site observations and interpretation from the results, construction noise is considered insignificant and below the noise limits level. It is therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. It was however recommended that the Contractor shall maintain the existing practices stipulated in the EIA Report in order to minimise the potential noise impact in future.

No Action Level exceedance of construction noise was recorded in the reporting month.

Summary of above exceedance investigation of the Project is provided in the following Section 7.2 and **Appendix L**.

4.3.4 General Observations

The construction site had been under normal operation during the noise monitoring period and no unusual operation was observed. Traffic noise had been noticed at the monitoring location during the noise monitoring period.

5 Landscape and Visual Monitoring

5.1 Landscape and Visual Monitoring Requirements

Monitoring Parameters

The landscape and visual conditions of the site and its vicinity shall be reviewed with regards to parameters assessed in the EIA Report, including landscape resources (LR), landscape character area (LCA) and view condition of visual sensitive receiver (VSR).

Monitoring Frequency and Location

The landscape and visual monitoring and audit shall be undertaken bi-weekly throughout the construction period. The components of each assessed parameter of LR, LCA and VSR are summarised in **Table 5.1**.

Table 5.1 Parameters of landscape resources, landscape character areas and landscape sensitive receivers assessed during baseline site survey

ID No.	Names
Landscape Resources	
LR1	Tsing Sin Playground
LR2	Roadside Planting along Tuen Mun Road Adjacent to Kam Fai Garden
LR3	Street trees along Castle Peak Road – Castle Peak Bay
LR4	Street trees along Tuen Mun Road west of Chi Lok Fa Yuen and east of On Ting Estate
LR5	Street trees along Tuen Mun Road west of Waldorf Garden and CMA Choi Cheung Kok Prevocational School
LR6	Street trees along Tuen Mun Road near Tuen Mun Town Plaza
LR7	Street trees along Tuen Mun Road east of Yan Oi Tong
LR8	Trees at roadside planting areas near Yan Oi Tong Circuit
LR9	Trees at planting area near Tuen Mun Town Plaza
LR10	Trees at planting area near New Town Mansion
LR11	Trees at planting area near On Ting Estate
LR12	Tsing Hoi Playground
Landscape Character Areas	
LZ1	Tuen Mun Residential Urban Landscape
LZ2	Tuen Mun Mixed Modern Comprehensive Urban Development Landscape
LZ3	Tuen Mun 'Hui' Urban Landscape
Visual Sensitive Receivers	
C/R1	Tuen Mun Town Plaza, Waldorf Garden
C/R2	Tuen Cultural Centre, Tuen Mun Town Plaza
C/R3	Chelsea Height
GIC1	Tuen Mun Church and Tuen Mun Tseng Choi Street Joint-user Complex
GIC2	Sin Hing Tong Temple
GIC3	Semple Memorial Secondary School and Chung Shing Benevolent Society Mrs. Aw Boon Haw Secondary School
GIC4	Car park (Open)
GIC5	Yan Oi Tong Community & Sports Centre
GIC6	Tuen Mun Government Secondary School, Choi Cheung Kok Secondary School

ID No.	Names
GIC7	Madam Lau Wong Fat Primary School, Lui Cheung Kwong College, Leung Kau Kui College, Lui Cheung Kwong Primary School, Wu Siu Kui Primary School
GIC8	Sam Shing Temple
O1	San Hui Playground
O2	Tsing Sin Playground
O3	Siu Lun Sports Ground
O4	Hoi Sin Playground
R1	Residential Area of Tuen Mun San Hui
R2	Residential Area along Yan Oi Tong Circuit
R3	On Ting Estate and Siu On Court
R4	Residential Area along Tsing Hoi Circuit
R5	Handsome Court, Alpine Garden, Hoi Tak Garden and Harvest Garden, Kam Fai Garden
R6	Siu Lun Court
R7	Goodview Garden and Tsui Ning Garden
R8	Sam Shing Estate
R9	Hanford Garden
T1	Tuen Mun Road – Vehicular and Pedestrian

5.2 Audit Results

In the reporting month, landscape and visual site audit in accordance with the requirements stipulated in the EIA report was conducted on 5 and 26 May 2011.

In accordance with the Landscape Plan of the Project under the Clause 2.13 of the Part C of the EP and updated information by the Contractor, a total of 1021 trees would be affected. 134 trees would be retained, 389 trees would be transplanted to Siu Lang Shui Road and 521 trees would be felled during the construction phase. The implementation and maintenance of landscape and mitigation measures, listed in EIA report, were checked during the site audit. No substantial change of LR, LCA and VSR was noted. No non-compliance has been triggered during the reporting month.

Since the commencement of the Project, total 478 trees were felled and the pruning of the transplanted trees was carried out in accordance with the Specification for Tree Protection and Transplanting Works in Landscape Plan. The updated statuses of the felled and transplanted trees during the reporting month are summarized in **Tale 5.2** and the summary report is presented in **Appendix I**.

Table 5.2 Status of felled and transplanted trees during reporting month

	No. of trees to be felled	No. of trees to be transplanted			
		Crown pruning	1 st root pruning	2 nd root pruning	3 rd root pruning
In progress	43	30	37	49	71
Completed	478	359	352	340	318
Total	521	389	389	389	389
Percentage completed (%)	92	92	90	87	82

In order to enhance the landscape and visual experience to Tuen Mun town centre neighborhood and compensate for the district tree felling, compensatory tree planting of 699 no. of trees would be carried out throughout various area in Tuen Mun after the discussion and agreement with Tuen Mun District Council (TMDC) and relevant government parties (e.g. LCSD).

5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures

The design, implementation and maintenance of landscape and visual mitigation measures stipulated in the EM&A manual, were checked during the site audits. No non-compliance has been triggered.

The Implementation Schedule of Mitigation Measures was inspected during the weekly site inspections in reporting month. The details of the findings/observations are described in Section 7.1. Summary of the implementation status of construction phase Landscape and Visual mitigation measures are presented in **Appendix C**.

5.4 Recommendations, Corrective Actions and Outstanding Issues

The recommendations, corrective actions or outstanding issues in relation with the landscape and visual monitoring are as follows:

- The Contractor was reminded to strip and store the topsoil for re-use in the construction of soft landscape works, where practical;
- The Contractor was reminded to protect the retained trees carefully during construction;
- The Contractor was reminded to transplant the trees which affected by the works where possible and practical;
- The Contractor was reminded to compensate the trees for felled trees;
- The Contractor was reminded to control of night-time lighting;
- The Contractor was reminded to erect a compatible decorative screen hoarding with the surrounding setting;
- The Contractor was reminded to avoid placing the construction materials too close to the trees.

6 Waste Disposal

The actual amounts of different types of waste generated by the activities of the Project during the reporting month are shown in Table 6.1. The monthly summary flow table is provided in **Appendix J**.

Table 6.1 Amount of waste generated in reporting month

Waste Type	Amount	Disposal Locations
Inert C&D Materials	0 m ³	Broken concrete
	0 m ³	Reused in the Contract
	0 m ³	Reused in other Projects
	2,968.875 m ³	Disposal of at public fill at Tuen Mun Area 38
Chemical Waste	0 kg	N/A
Paper / cardboard packaging	371 kg	Recycler
Plastic	0 kg	
Metal	0 kg	
General Refuse	53.625 m ³	Disposal of at WENT landfill

7 Environmental Performance

7.1 Environmental Site Inspection

Environmental site inspections were carried out on a weekly basis to monitor environmental issues on the construction sites to ensure that all mitigation measures were implemented timely and properly. A summary of the site inspections in the reporting month is presented in **Table 7.1**.

Table 7.1 Key findings of weekly environmental site audit in the reporting month

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
Air Quality Mitigation Measures				
Yan Oi Tong Street	12 May 11	Excessive emission from a mobile crane was observed, the Contractor was reminded to carry out proper maintenance.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
Yan Oi Tong Street and Tuen Hing Road	12 May 11	The Contractor was reminded to minimize the gaps between cover sheets of the cement store.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
Rosedale Garden and Tuen Hing Road	12 May 11	The Contractor was reminded to increase the water spray frequency for minimise dust impact.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
				19 May 11.
Tuen Fat Road	19 May 11	Dark smoke emission generator was observed. The Contractor should inspect the machine maintenance and fix it as soon as possible.	Agreed with the ET's advice.	Dark smoke emission was not observed. Closed on 26 May 11.
Tuen Hi Road	26 May 11	Dark smoke emission from pilling machine was observed. The Contractor should enhance the machine maintenance and fix it as soon as possible.	Agreed with the ET's advice.	Dark smoke emission was not observed. Closed on 2 Jun 11.
Water Quality Mitigation Measures				
Yan Ching Street	5 May 11	Stagnant water within the site area should be removed as soon as possible to avoid mosquito breeding.	Agreed with the ET's advice.	Stagnant water was removed. Closed on 12 May 11.
Yan Chin Bridge/Yan Oi Tong Street	12 May 11	The contractor was reminded to desilt the U Channel along TMR.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
All area	12 May 11	The Contractor was reminded to carry out proper temporary drainage control to comply with WPCO requirements.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
Yan Ching Street (near Yan Oi Tong Circuit); & Area under Wong Chu Road Flyover	19 May 11	The Contractor should enhance the cleaning frequency of the U-Channel to avoid any silt/sand accumulation.	Agreed with the ET's advice.	U-channel had been cleaned. Closed on 26 May 11.
Tuen Fat Road	19 May 11	The Contractor was reminded to extend the sand bags bunding along the site bounding (Tuen Fat Road) and enhance the inspection to avoid any surface runoff overflowing to public area.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 26 May 11.
Yan Oi Tong Street	12 May 11	The Contractor was reminded to place the sands bags at both ends of site entrance (including Rosedale Garden)	Agreed with the ET's advice.	The reminder had been noted by Contractor.

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
				Closed on 19 May 11.
Tuen Hi Road	26 May 11	The Contractor should enhance the inspection of sandbags condition and replace the damaged sandbags as soon as possible. In addition, the Contractor was reminded to provide additional bunding between pilling areas and haul road.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 2 Jun 11.
Waste Management				
Yan Oi Tong Circuit	5 May 11	The waste cement bags should be removed regularly to avoid accumulation. Tarpaulin covering should be provided before disposal to avoid dust disturbance.	Agreed with the ET's advice.	The waste cement bags had been removed. Closed on 12 May 11.
Pui To Road	5 May 11	Drip tray should be provided for the chemicals placing.	Agreed with the ET's advice.	Chemicals had been removed. Closed on 12 May 11.
Tsing Hoi Circuit	5 May 11	The stockpiles should not be placed too close to the TMR without barrier/bunding to avoid the loose soil dropping to TMR.	Agreed with the ET's advice.	Stockpiles had been removed. Closed on 12 May 11.
	26 May 11	Accumulated debris and construction waste should be removed regularly to avoid accumulation.	Agreed with the ET's advice.	Debris and construction waste had been removed. Closed on 2 Jun 11.
Rosedale Garden	12 May 11	The drip tray of air compressor (no.62) contained oil-bearing wastewater. The Contractor was reminded to remove it as chemical waste.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
		Oil leakage was observed at a Boring Machine (TMT-113). The Contractor was reminded to remove the contaminated soil as chemical waste and carry out proper maintenance of the machine.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 19 May 11.
Tuen Hing Road	12 May 11	The Contractor was reminded to dispose of the rubbish (at site entrance) as soon as possible.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
				19 May 11.
General				
Entire site area	5 May 11	The Contractor was reminded to update the new version Environmental Permit as soon as possible and display on the Project site entrance/exits.	Agreed with the ET's advice.	The reminder had been noted by Contractor. Closed on 12 May 11.

7.2 Complaint Record

One environmental complaint regarding the cleaning water spillage to TMR was recorded in the reporting month.

The complaint was received by the ICC and ET on 23 and 24 May 2011 respectively regarding the cleaning water spillage to TMR (section between Pui To Road and Yan Oi Tong).

As confirmed by the Contractor and Supervising Officer's Representative, the floor cleaning activities was carried out at the site entrance of Pui To Road during the complaint period. The cleaning water was spilled to TMR and affected the travelling vehicles. Therefore, it is concluded that the complaint was work-related under the Project.

As advised by the Contractor and Supervising Officer's Representative, the workers were reminded to pay attention during cleaning activities to avoid water spillage to TMR after the complaint was received. Based on the weekly site inspections on 26 May and 2 June 11, the site condition was satisfactory and no water spillage was observed.

Nevertheless, ET recommended that the Contractor should undertake following mitigation measures to minimize the nuisance.

1. Improve the working practices to minimize the nuisance during the cleaning activities as far as possible; and
2. Enhance the workers awareness by regular training to minimize nuisance during the cleaning activities.

The updated statistical summary of complaint is presented in **Table 7.2**. The updated complaint log (C005) of the Project in the reporting month is shown in **Appendix L**.

Table 7.2 Summary of complaints for the contract

Reporting Period	Complaint Statistics		Area of Concern	Validity to the Project	Status
	Number	Cumulative			
02/08/10 – 31/10/10	0	0	-	-	-
01/11/10 – 30/11/10	1	1	Noise	Yes (Ref.: C001)	Closed on 30 Nov 10.
01/12/10 – 31/01/11	0	1	-	-	-
01/02/11 – 28/02/11	1	2	Noise	Yes (Ref.: C002)	Closed on 2 Mar 11.
01/03/11 –	0	2	-	-	-

Reporting Period	Complaint Statistics		Area of Concern	Validity to the Project	Status
	Number	Cumulative			
31/03/11					
01/04/11 – 30/04/11	2	4	Water	Yes (Ref.: C003)	Closed on 16 Apr 11.
			Noise	Yes (Ref.: C004)	Closed on 16 May 11.
01/05/11 – 31/05/11	1	5	Water	Yes (Ref.: C005)	Closed on 10 Jun 11.

7.3 Notification of Summons and Successful Prosecution

No summons or prosecutions related to environmental issues were received or made against the Project in the reporting month.

7.4 Review of Reasons of Non-Compliance

Nine limit level exceedances of noise monitoring were recorded from the monitoring data at locations N1, N2 and N6, which triggered the Event and Action Plan for remedial action. Based on the on-site observations and interpretation from the results, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road and was not related to the construction activities. No particular remedial work is required.

8 Future Key Issues

8.1 Key Issues for the Coming Month

Key issues to be considered in the coming month include:

- Dust generation from activities on-site, such as vehicular movements along unpaved area, excavation and demolition;
- Noise impact from operating equipment and machinery on-site;
- Muddy surface runoff overflow to public area;
- Uncontrolled water discharge into nearby water body;
- Storage and using of chemicals/fuel and chemical waste/waste oil on site;
- Disposal of construction waste; and
- Tree maintenance.

8.2 Environmental Monitoring Program for the Coming Month

Environmental monitoring and audit will be carried out in accordance with the requirements stipulated in the EM&A manual. Tentative air, noise, landscape and visual monitoring as well as weekly site audit schedule for the coming month with respect to the construction programme is shown in **Appendix K**.

The construction programme for the coming month is shown in **Table 8.1**.

Table 8.1 Tentative programme of construction works

Month	Locations	Details of Construction Works
June 2011	Various locations	Site clearance, site hoarding construction, tree transplanting, ground investigation, pilling works, temporary footbridge construction and underground utilities diversion

9 Conclusions and Recommendations

9.1 Conclusions

The construction phase of the Project was commenced on 2 August 2010. The EM&A programme has been implemented since then, including air quality, noise, landscape and visual and environmental site audits.

No Action and Limit Level exceedance was recorded for impact air quality in the reporting month.

Nine Limit level exceedances of noise monitoring were recorded from the monitoring data at locations N1, N2 and N6, which triggered the Event and Action Plan for remedial action. Based on the on-site observations and interpretation from the results, noise exceedance was not related to the construction activities. No particular remedial work is required. No Action Level exceedance of construction noise was recorded in the reporting month.

One environmental complaint regarding the cleaning water spillage was recorded in the reporting month. After the investigation, it is concluded that the complaint was attributable to the Contractor. The corresponding mitigation measure due to the complaint was recommended to be carried out by the Contractor.

No summons or prosecution related to environmental issues was received during the reporting month.

In accordance with the requirements stipulated in the EM&A manual, landscape and visual site audit was conducted on 5 and 26 May 2011. Total 478 trees were felled and the pruning of the transplanted trees was carried out during the reporting month. No substantial change of LR, LCA and VSR was noted.

Four (4) weekly environmental site audits were carried out during the reporting month. The major environmental concerns were related to air quality, noise, water quality, waste management and tree maintenance.

9.2 Recommendations

Impact monitoring will be continued to carry out in the following month and followed by the requirement stipulated in the EM&A manual. Attention will be paid to environmental issues identified in EIA report and weekly site audit. Mitigation measures recommended in EIA report and Implementation Schedule of Mitigation Measure will be fully implemented.

Construction noise is one of the key environmental issues especially in restricted hours. The conditions stipulated in CNPs should be strictly followed when the construction works were carried out during the restricted hours.

Construction dust is another key environmental issue. The implemented construction dust mitigation measures including covering of exposed slope / soil with tarpaulin sheet etc., should be maintained and improved as necessary. Adequate water spraying should be provided for the unpaved area to minimize dust disturbance.

Water quality impact is also key environmental issue. The drainage system should be well maintained. All wastewater generated within the site should be collected and treated prior to discharge. The solid and liquid waste management should be strictly followed in accordance with the requirements described in the EIA report.

10 Reference

- [1] AECOM Asia Co. Ltd. December 2008. Agreement No. CE 22/2005 (HY) Supplementary No. 1 Traffic Improvements to Tuen Mun Road Town Centre Section – Environmental Monitoring & Audit Manual.

- [2] Ove Arup & Partners Hong Kong Limited. July 2010. Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section – Baseline Monitoring Report (Revision_4).

Appendix A

**Construction
Programme**

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

[illegible]

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

08-Jun-11?

[illegible]

3 Months Rolling Programme (cutoff: 31-05-11)		Checked		Approved	
		Date	Revision		
Remaining Level of Effort	Actual Work	06-May-11	1104	Tim	
Actual Level of Effort	Remaining ...	08-Jun-11	1105	Tim	

Page 2 of 8

[illegible]

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

08-Jun-11?

Item No.	Item Description	Unit	Quantity	Unit Price	Total Price	Remarks
RA100	Reinforcement steel (HRB335) for NE24	m³	60	1500	90000	Reinforcement steel (HRB335) for NE24
RA101	Drainage diversion for existing 450 dia pipe for NE24	m³	60	2500	150000	Drainage diversion for existing 450 dia pipe for NE24
RA102	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA103	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA104	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA105	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA106	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA107	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA108	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA109	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA110	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA111	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA112	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA113	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA114	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA115	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA116	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA117	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA118	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA119	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA120	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA121	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA122	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA123	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA124	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA125	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA126	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA127	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA128	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA129	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA130	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA131	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA132	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA133	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA134	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA135	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA136	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA137	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA138	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA139	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA140	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA141	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA142	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA143	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA144	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA145	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA146	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA147	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA148	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA149	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA150	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA151	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA152	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA153	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA154	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA155	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA156	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA157	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA158	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA159	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA160	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA161	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA162	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA163	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA164	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA165	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA166	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA167	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA168	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA169	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA170	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA171	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA172	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA173	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA174	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA175	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA176	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA177	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA178	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA179	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA180	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA181	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA182	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA183	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA184	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA185	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA186	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA187	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA188	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA189	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA190	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA191	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA192	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA193	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA194	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA195	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA196	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA197	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA198	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA199	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA200	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA201	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA202	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA203	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA204	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA205	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA206	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA207	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA208	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA209	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA210	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA211	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA212	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA213	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA214	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA215	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA216	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA217	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA218	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA219	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA220	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA221	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA222	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA223	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA224	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA225	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA226	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA227	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA228	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA229	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA230	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA231	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA232	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA233	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA234	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA235	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA236	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA237	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA238	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA239	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA240	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA241	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA242	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA243	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA244	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA245	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA246	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA247	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA248	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA249	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA250	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA251	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA252	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA253	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA254	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA255	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA256	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA257	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA258	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA259	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA260	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA261	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA262	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA263	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA264	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA265	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA266	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA267	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA268	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA269	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for NE24
RA270	Contracted pile cap for NE24	m³	60	2500	150000	Contracted pile cap for

3 Months Rolling Programme (cutoff: 31-05-11)		Date	Revision	Checked	Approved
Remaining Level of Effort	Actual Work	06-May-11	1104	Tim	
Actual Level of Effort	Remaining ...	08-Jun-11	1105	Tim	

Page 4 of 8

18

[illegible]

3 Months Rolling Programme (cutoff: 31-05-11)		Date	Revision	Checked	Approved
Remaining Level of Effort	Actual Work	06-May-11	1104	Tim	
Actual Level of Effort	Remaining ...	08-Jun-11	1105	Tim	

Page 5 of 8

[illegible]

08-Jun-11?

10

[illegible]

Remaining Level of Effort	Actual Work	3 Months Rolling Programme (cutoff: 31-05-11)				Approved
Actual Level of Effort	Remaining ...	Date	Revision	Checked		
		06-May-11	1104	Tim		
		08-Jun-11	1105	Tim		

Page 8 of 8

Appendix B

**Environmental
Monitoring Programme
in the Reporting Month**

Agreement No. CE 22/2005 (HY) Traffic Improvement to Tuen Mun Road Town Centre Section
Tentative Impact Monitoring Schedule - May 2011 Revision 1

Date		Air Quality	Noise	Landscape & Visual	Site Inspection
		24-hours TSP	L _{Aeq} , 30 min		
1-May-11	Sun				
2-May-11	Mon				
3-May-11	Tue				
4-May-11	Wed				
5-May-11	Thu				
6-May-11	Fri				
7-May-11	Sat				
8-May-11	Sun				
9-May-11	Mon				
10-May-11	Tue				
11-May-11	Wed				
12-May-11	Thu				SSEMC
13-May-11	Fri				
14-May-11	Sat				
15-May-11	Sun				
16-May-11	Mon				
17-May-11	Tue				
18-May-11	Wed				
19-May-11	Thu				
20-May-11	Fri				
21-May-11	Sat				
22-May-11	Sun				
23-May-11	Mon				
24-May-11	Tue				
25-May-11	Wed				
26-May-11	Thu				
27-May-11	Fri				
28-May-11	Sat				
29-May-11	Sun				
30-May-11	Mon				
31-May-11	Tue				

	Public Holiday
	Monitoring Day

Monitoring Details

Monitoring	Quantity	Locations	Parameters
Air Quality	6	Mrs.Aw Boon Haw Secondary School Tai Tung Pui Social Service Building Wu Siu Kui Primary School Choi Cheung Kok Secondary School Tuen Mun Town Hall Yan Oi Tong Community and Sport Centre	24-hour TSP, Wind speed / direction
Noise	6	Kam Fai Garden Tai Tung Pui Social Service Building Yuen Yuen Primary School Wu Siu Kui Primary School Tuen King Building Choi Cheung Kok Secondary School	L _{Aeq} (30 min), L ₁₀ , L ₉₀

Appendix C

Implementation Schedule of Mitigation Measures

Summary of Implementation Schedule of Mitigation Measures

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Noise Control		
3.8.1	2.8.1	<p>Good site practice and management can significantly reduce the noise impact of construction site activities on nearby NSRs</p> <ul style="list-style-type: none"> • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works; • machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs; • mobile plant should be sited as far away from NSRs as possible; and • material stockpiles and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
3.8.4	2.8.3	Use of quieter mechanical equipment	Works Sites / During Construction Phase	✓
3.8.9	2.8.4	<p>Provision of movable noise barrier in the vicinity of the following NSRs</p> <ul style="list-style-type: none"> • FEC (Far East Consortium Tuen Mun Central Building) • FM (Forward Mansion) • HTB (Hing Tai Building) • TMTP1 (Tuen Mun Town Plaza) • WG2 (Waldorf Garden) • CMA (CMA Choi Cheung Kok Secondary School) • LWF (Yan Oi Tong Madam Lau Wong Fat Primary School) • TMF (Tuen Mun Fa Yuen) • LCK (Lui Cheung Kwong Lutheran College) • CLFY1 (Chi Lok Fa Yuen) 	Works Sites from the listed NSRs / During Construction Phase	N/O

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<ul style="list-style-type: none"> TFH (On Ting Estate (Ting Fuk House)) LCKP (Lui Cheung Kwong Lutheran Primary School) TTP (Tung Wah Group of Hospitals Tai Tung Pui Social Service Building) CSBS (CSBS Mrs. Aw Boon Haw Secondary School) KFG3D (Kam Fai Garden) 		
3.8.12	2.8.5	<p>Site clearance and the following activities not to be undertaken in the vicinity of the NSR LCK so as to reduce construction noise impact during normal teaching hours.</p> <ul style="list-style-type: none"> truck would not operate concurrently with other PME's during tree transplanting and noise barrier foundation work. tree transplanting would not be undertaken concurrently with bulk excavation and utilities diversion. construction of storm water drain would not be undertaken concurrently with noise barrier/enclosure foundation. construction of sub-base and road base would not be undertaken concurrently with noise barrier/enclosure installation. road surfacing, construction of road kerbs, central dividers, parapets, and installation of crash cushion and sign gantry would not be undertaken concurrently. installation of gantry and directional lighting, and street lighting would not be undertaken concurrently. 	Work site in the vicinity of Lui Cheung Kwong Lutheran College (LCK) / Stage 2 (Ch. 28050 – 28200 of TMR) during Construction Phase	N/O

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
3.8.13	2.8.6	Liaise with all the relevant schools to check out their examination periods and activities in the beginning of the work programme in order to make good planning and arrangement of works and provide sufficient mitigation plans to alleviate noise impacts.	CMA Choi Cheung Kok Secondary School (CMA), Yan Oi Tong Madam Lau Wong Fat Primary School (LWF), Lui Cheung Kwong Lutheran College (LCK), Lui Cheung Kwong Lutheran Primary School (LCKP) and CSBS Mrs. Aw Boon Haw Secondary School (CSBS) / During Construction Phase	✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Air Quality Control</i>		
4.8.1	3.11.2	<p>Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation.</p> <ul style="list-style-type: none"> • skip hoist for material transport should be totally enclosed by impervious sheeting • every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site • the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores • where a site boundary adjoins a road, streets or other accessible to the public, hording of not less than 2.4m high from ground level should be provided along the entire length except for a 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		site entrance or exit <ul style="list-style-type: none"> every stack of more than 20 bags of cement should be covered entirely by impervious sheeting places in an area sheltered on the top and the 3 sides all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet the height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. 		✓ Rdr ✓ ✓ ✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Water Quality Control		
5.8.2	4.3.2	Construction run-off and Drainage <ul style="list-style-type: none"> Silt removal facilities such as silt traps or sedimentation facilities should be provided to remove silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Careful programming of the works to minimise surface excavations for the road improvement works during the wet season. If excavation of soil cannot be avoided during the wet season, exposed slope surfaces should be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarized in ProPECC PN 1/94. Exposed soil surfaces should be protected by paving or fill material as soon as possible to 	Works Sites / During Construction Phase	✓ ✓ ✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<p>reduce the potential of soil erosion.</p> <ul style="list-style-type: none"> Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. These materials should not be placed near water courses. 		✓
5.8.3 - 5.8.4	4.3.3	<p>General Construction Activities</p> <ul style="list-style-type: none"> Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering the nearby local stormwater drainage system. Stockpiles of cement and other construction materials should be kept covered when not being used. Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event 	Works Sites / During Construction Phase	<p>Obs</p> <p>✓</p> <p>✓</p>
5.8.5	4.3.4	<p>Sewage from Construction Workforce</p> <ul style="list-style-type: none"> Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities 	Works Sites / During Construction Phase	✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Waste Management</i>		
6.6.1	5.2.2	<p><i>Good Site Practices</i></p> <ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site. Training of site personnel in proper waste management and chemical waste handling procedures. Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites). 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>Obs</p> <p>✓</p>
6.6.5	5.2.6	<p><i>Chemical Wastes</i></p> <ul style="list-style-type: none"> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTC or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p>
6.6.6	5.2.7	<p><i>General Refuse</i></p> <ul style="list-style-type: none"> General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
6.6.2	5.2.3	<p><i>Waste Reduction Measures</i></p> <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> • Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. • Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. • Any unused chemicals or those with remaining functional capacity shall be recycled. • Use of reusable non-timber formwork to reduce the amount of C&D material. • Prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill. • Proper storage and site practices to minimise the potential for damage or contamination of construction materials. • Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
6.6.4	5.2.5	<p><i>Construction and Demolition (C&D) Material</i></p> <ul style="list-style-type: none"> • The excavated fill material shall be re-used on-site as backfill material as far as possible. • The surplus excavated material should be disposed of at the designated public fill reception facility, as agreed with the Secretary of the Public Fill Committee, for other beneficial uses. • C&D waste would require disposal to the designated landfill site. • In order to monitor the disposal of C&D materials at the public fill reception facility and landfill and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Ecology		
7.9.2	6.2.2	Construction activities should be confined to developed areas of low ecological value, and there should be no direct impact on other habitats within the Study Area.	Works Sites / During Construction Phase	✓
7.9.3	6.2.3	Noise mitigation measures, including installation of noise-emitting construction plant away from egret, careful scheduling of noisy works with high disturbance impact to avoid breeding season of ardeid species (i.e. mid March to August) to prevent impacts on nesting activities of Little Egret, operation of well-maintained machinery, careful programming of works and use of noise reduction facilities could be implemented to mitigate noise impacts arising from construction activities such as road widening and road paving. Temporary noise barrier should also be used to reduce the level of noise during construction. Noise impact would be minimised during operation phase as permanent noise barrier has been proposed to be constructed. The use of low noise road surfacing could also reduce the level of noise during operation.	Works Sites / During Construction Phase	✓
7.9.4	6.2.4	In order to minimise the impact of construction dust to the vegetation and associated wildlife within and around the proposed Works Area, the following mitigation measures should be implemented: <ul style="list-style-type: none"> • regular watering • complete coverage of dusty material storage piles • the use of minimum practical height for dropping excavated material 	Works Sites / During Construction Phase	✓ ✓ ✓
7.9.6	6.2.6	To minimise the indirect impacts to the nearby Tuen Mun River Channel, the following mitigation measures should be implemented: <ul style="list-style-type: none"> • Site runoff could be directed towards regularly cleaned and maintained sand traps, silt traps and where appropriate • Oil/grease separators to minimise risk of sedimentation and pollution to the river channel. • Debris and rubbish generated on-site should be collected, handled and disposed properly. 	Works Sites / During Construction Phase	✓ N/O ✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
7.9.5	6.2.5	Standard good site practice measures should be implemented and should include: <ul style="list-style-type: none"> • Placement of equipment in designated Works Areas within the existing disturbed land. • Construction activities should be restricted to the proposed Works Area. • The proposed Works Area should be reinstated immediately after completion of the works. • Open burning on proposed works site is illegal, and will be strictly enforced. • Waste skips should be provided to collect general refuse and construction wastes, which should be disposed regularly and properly off-site. • Soil contaminated by fuel leaked from construction plants should be removed and treated. 	Works Sites / During Construction Phase	✓ ✓ ✓ ✓ ✓ N/O
7.9.7	6.2.7	To minimise the chance of bird collision during operation phase, falcon sticker, tinted materials, embedded opaque stripes and superimposed patterns of thin opaque stripes are methods that could be used during the design of noise barrier.	Works Sites / During Operation Phase	N/O
7.9.8	6.2.8	Compensatory planting is recommended as the current roadside plantation must be removed to give way to the works. Species of choice should be composed of similar native species and the felling and planting ratio should be no less than 1:1 in terms of quantity.	Works Sites / During Operation Phase	N/O

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Landscape and Visual</i>		
Table 8.8	7.3.1	CM1 Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Works Sites / During Construction Phase	✓
Table 8.8	7.3.1	CM2 Existing trees to be retained on site should be carefully protected during construction.		Obs
Table 8.8	7.3.1	CM3 Trees unavoidably affected by the works should be transplanted where practical.		✓
Table 8.8	7.3.1	CM4 Compensatory tree planting should be provided to compensate for felled trees.		✓
Table 8.8	7.3.1	CM5 Control of night-time lighting.		✓
Table 8.8	7.3.1	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.		✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Land Contamination</i>		
9.8.3	8.2.2	<p>To minimize construction workers' potential contact with the contaminated materials</p> <ul style="list-style-type: none"> • The use of bulk earth-moving excavator equipment would minimise construction workers' potential contact with the contaminated materials; • Exposure to any contaminated materials can be minimised by the wearing of appropriate clothing and personal protective equipment such as gloves (when interacting directly with suspected contaminated material), providing adequate hygiene and washing facilities and preventing smoking and eating during such activities; • Stockpiling of contaminated soil should be avoided as far as possible. If this cannot be avoided, the stockpile of contaminated materials should be segregated from the uncontaminated ones. Moreover, the contaminated materials should be properly covered with waterproof material (e.g. tarpaulin sheet) to avoid leaching of contaminants, especially during rainy season. • Vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates should be sealed to prevent any leakage during transport or during wet conditions; • Only licensed waste haulers should be used to collect and transport any contaminated material to an appropriate disposal site and procedures should be developed to ensure that illegal disposal of waste does not occur; • Necessary waste disposal permits should be obtained, as required, from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 35), as required; • Records of the quantities of wastes generated and disposed of should be maintained; Adequate washing facilities should be provided on site; and • In accordance with good construction practice, silt traps should be used to reduce the impact to drainage caused by suspended solids arising from disturbed ground, or any construction materials such as cement and gravel. Groundwater should be disposed of in accordance with the Water Pollution Control Ordinance (Cap 358). 	Excavation zones / During excavation	N/O

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

Appendix D

Calibration Certificates and Spreadsheets of Air Monitoring Equipments



TISCH ENVIRONMENTAL, INC.
145 SOUTH MIAMI AVE.
VILLAGE OF CLEVELAND, OH 44102
513.467.9000
877.263.7610 TOLL FREE
513.467.9009 FAX
WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Mar 03, 2010 Rootsmeter S/N 9833620 Ta (K) - 292
Operator Tisch Orifice I.D. - 1378 Pa (mm) - 749.3

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4040	3.2	2.00
2	NA	NA	1.00	0.9880	6.4	4.00
3	NA	NA	1.00	0.8840	8.0	5.00
4	NA	NA	1.00	0.8420	8.8	5.50
5	NA	NA	1.00	0.6950	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)		Va	(x axis) Qa	(y axis)
1.0019	0.7136	1.4186		0.9957	0.7092	0.8828
0.9976	1.0097	2.0062		0.9915	1.0035	1.2485
0.9953	1.1260	2.2430		0.9892	1.1190	1.3959
0.9943	1.1809	2.3524		0.9882	1.1737	1.4640
0.9890	1.4230	2.8372		0.9829	1.4142	1.7657
Qstd slope (m) = 2.00078				Qa slope (m) = 1.25285		
intercept (b) = -0.01075				intercept (b) = -0.00669		
coefficient (r) = 0.99999				coefficient (r) = 0.99999		
y axis = SQRT[H2O(Pa/760) (298/Ta)]				y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
Qa = Va/Time


For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}



TISCH ENVIROMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVES, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

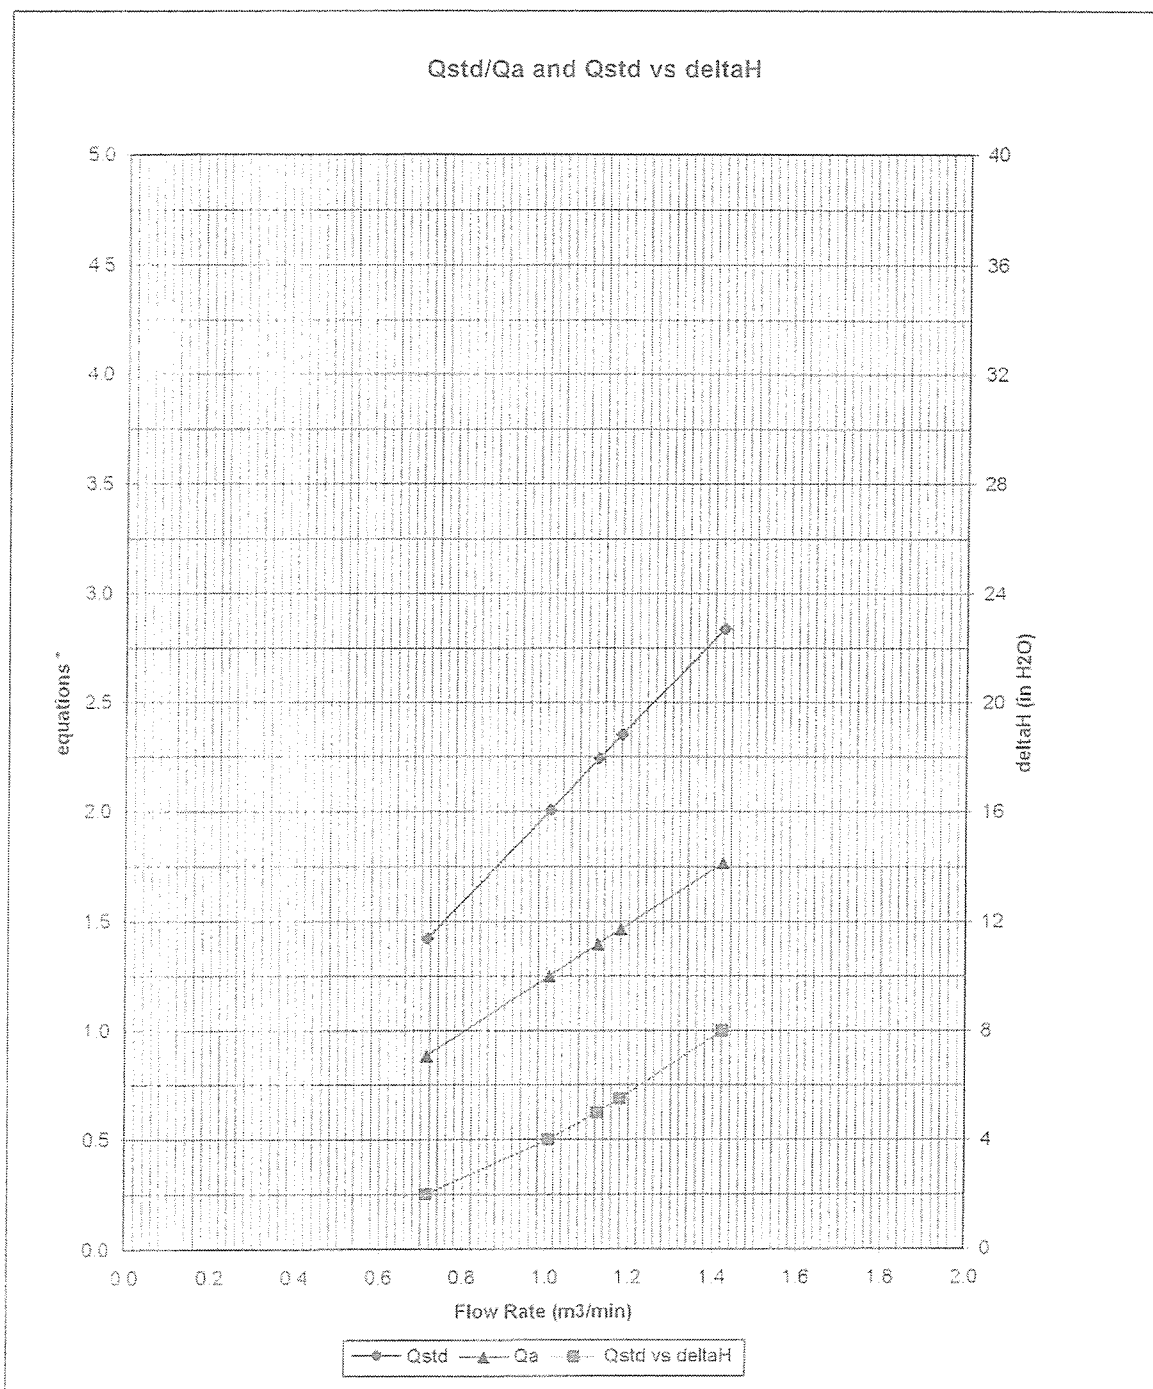

* y-axis equations:

Qstd series:

$$\sqrt{\Delta H \left(\frac{P_a}{P_{std}} \right) \left(\frac{T_{std}}{T_a} \right)}$$

Qa series:

$$\sqrt{\Delta H (T_a / P_a)}$$


#1378

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Tai Tung Pui Social Service	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	522	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.80	30.00	0.85	30.29
7	4.40	38.00	1.06	38.37
10	7.70	46.00	1.41	46.45
13	9.80	52.00	1.59	52.51
18	11.60	56.00	1.72	56.55

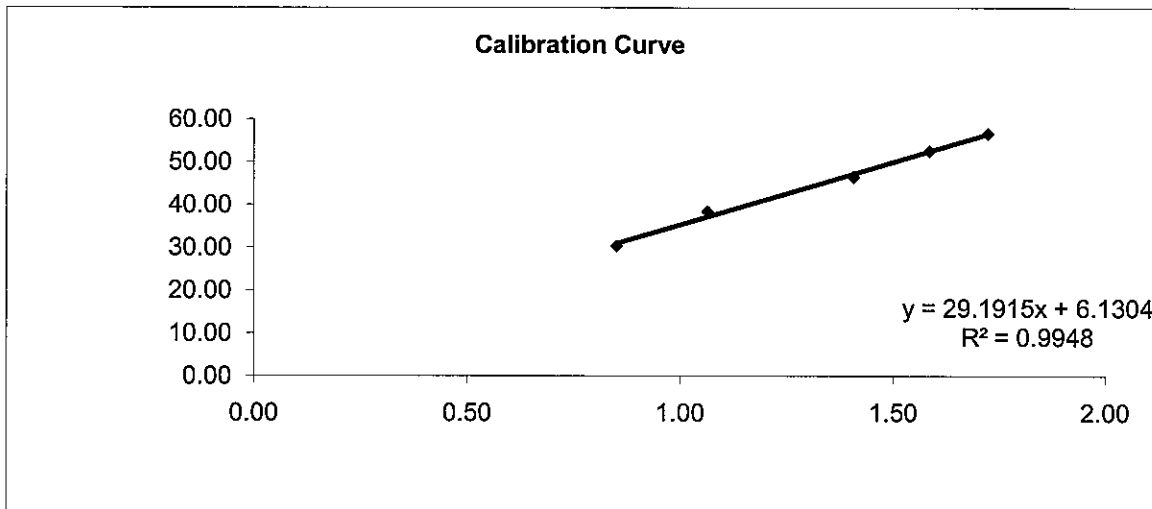

Linear Regression
 Sampler slope (m) : **29.1915**
 Sampler intercept (b) : **6.1304**
 Correlation coefficient (R²) : **0.9948**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Wu Siu Kui Primary School	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	505	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.90	30.00	0.86	30.29
7	4.40	36.00	1.06	36.35
10	7.50	46.00	1.39	46.45
13	9.60	52.00	1.57	52.51
18	12.00	60.00	1.75	60.59

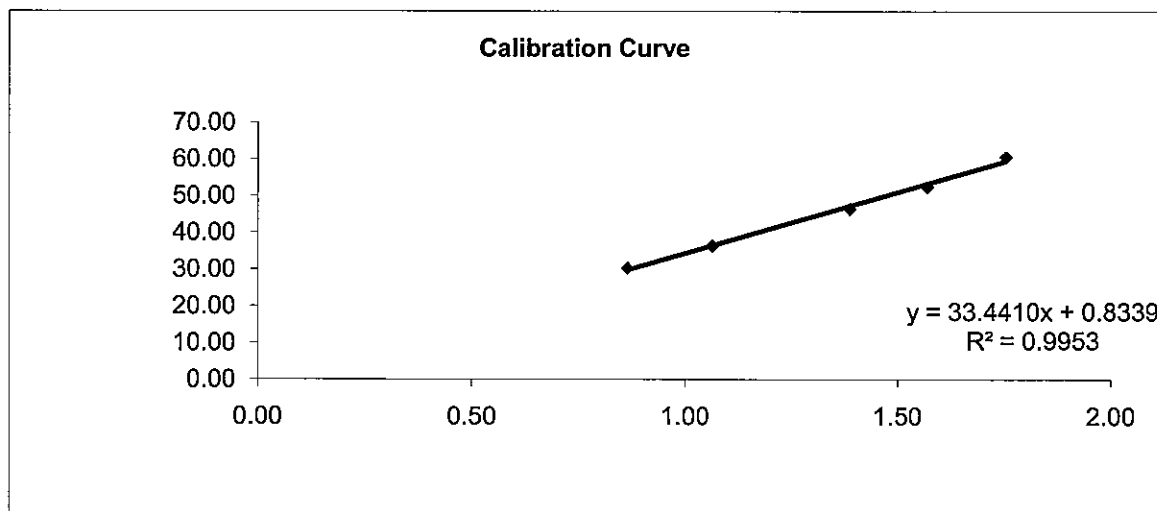

Linear Regression
 Sampler slope (m) : **33.4410**
 Sampler intercept (b) : **0.8339**
 Correlation coefficient (R²) : **0.9953**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Choi Cheung Kok Secondary	Temperature (K)	293 K
Sampler model	Thermo Anderson	P _{std}	760 mm Hg
Sampler serial number	1278	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.00	30.00	0.88	30.29
7	4.70	39.00	1.10	39.38
10	7.60	48.00	1.40	48.47
13	10.60	54.00	1.65	54.53
18	12.80	60.00	1.81	60.59

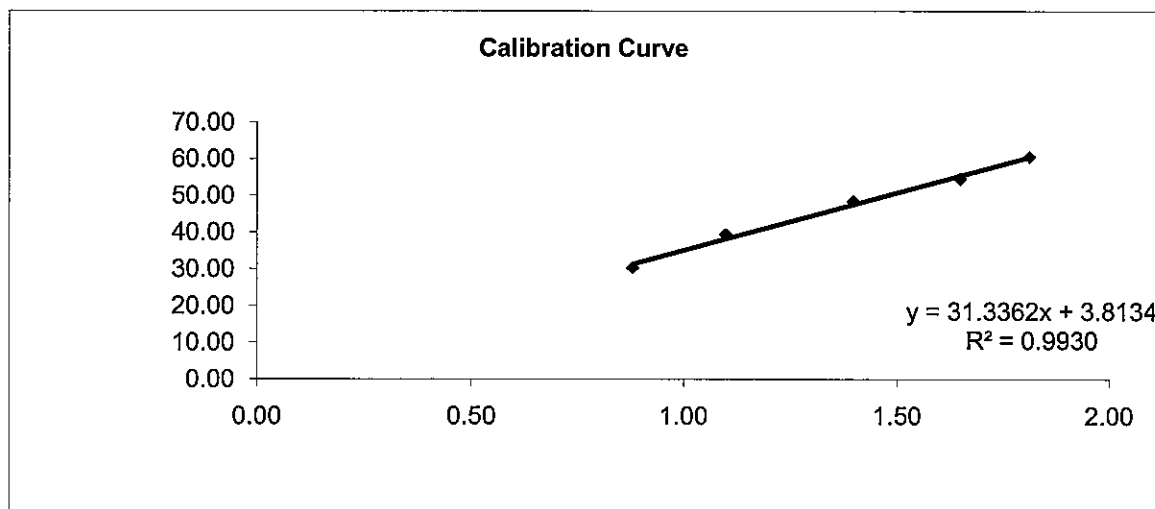

Linear Regression

Sampler slope (m) :	31.3362
Sampler intercept (b) :	3.8134
Correlation coefficient (R ²) :	0.9930

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Tuen Mun Town Hall	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	516	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.20	32.00	0.91	32.31
7	4.40	38.00	1.06	38.37
10	7.60	46.00	1.40	46.45
13	9.60	53.00	1.57	53.52
18	11.60	56.00	1.72	56.55

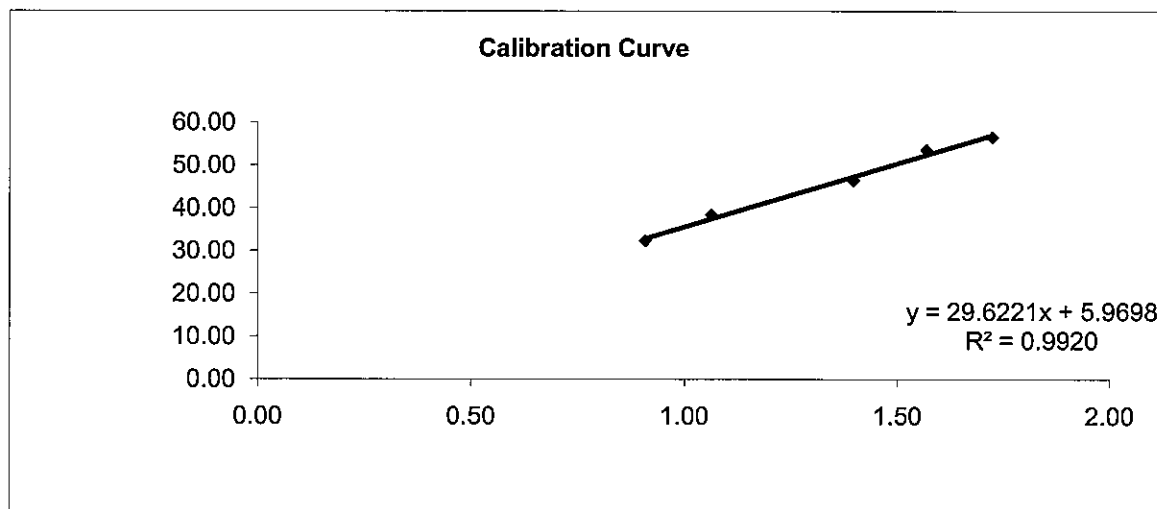

Linear Regression

Sampler slope (m) :	29.6221
Sampler intercept (b) :	5.9698
Correlation coefficient (R ²) :	0.9920

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____

Date: 1/4/11


Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date 1-Apr-11
 Next Calibration date 31-May-11
 Sampler location Yan Oi Tong
 Sampler model TE-5170
 Sampler serial number 510

Barometric pressure 762 mm Hg
 Temperature (°C) 20 °C
 Temperature (K) 293 K
 P_{std} 760 mm Hg
 T_{std} 298 K

Calibrator model GMW-2535
 Calibrator serial number 1378
 Slope of the standard curve, m_s 2.00078
 Intercept of the standard curve, b_s -0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.20	30.00	0.91	30.29
7	4.80	38.00	1.11	38.37
10	8.00	46.00	1.43	46.45
13	10.20	54.00	1.62	54.53
18	12.40	60.00	1.78	60.59

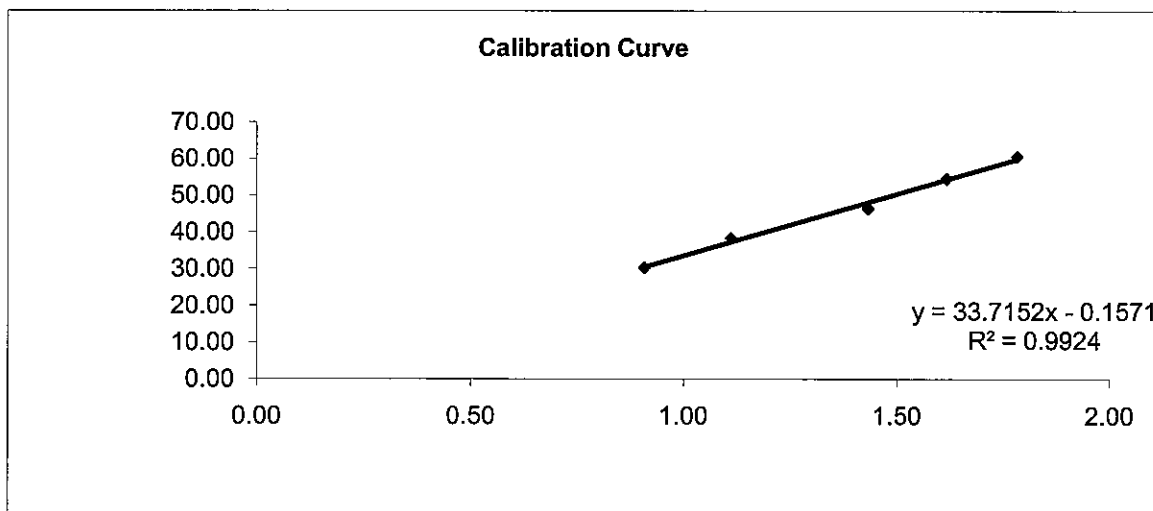

Linear Regression

Sampler slope (m) : 33.7152
 Sampler intercept (b) : -0.1571
 Correlation coefficient (R²) : 0.9924

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Mrs. AW Boon Haw Secondary School	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	521	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.90	32.00	0.86	32.31
7	4.20	38.00	1.04	38.37
10	7.60	46.00	1.40	46.45
13	10.20	54.00	1.62	54.53
18	11.60	58.00	1.72	58.57

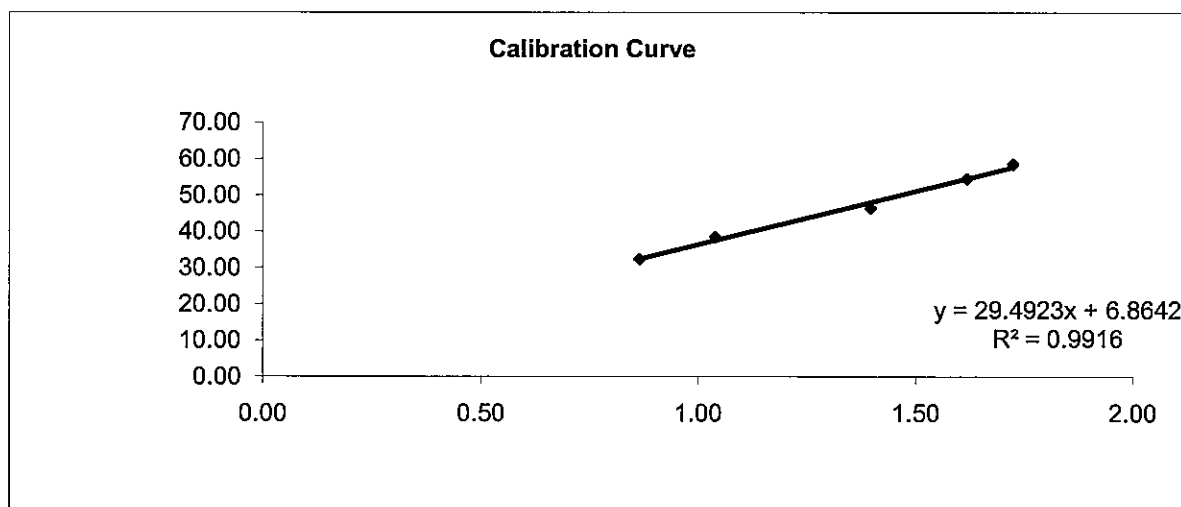

Linear Regression

Sampler slope (m) : **29.4923**
 Sampler intercept (b) : **6.8642**
 Correlation coefficient (R²) : **0.9916**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____

Date: 1/4/11

Appendix E

**Impact Air Quality
Monitoring Results**

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Mrs Aw Boon Haw Secondary School (AM1) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time (mins.)	Total vol. (m³)	(ug/m³) AM1
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130361	May-11	5-May-11	AM1	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7804	2.8616	0.0812	1.4662	1.4553	1.4608	11137.30	11161.30	1440.00	2103.48	38.6
130367	May-11	11-May-11	AM1	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.7781	2.8232	0.0451	1.4447	1.4458	1.4453	11161.30	11185.30	1440.00	2081.16	21.7
130373	May-11	17-May-11	AM1	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.7753	2.8308	0.0555	1.4662	1.4622	1.4642	11185.30	11209.30	1440.00	2108.45	26.3
130379	May-11	23-May-11	AM1	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7854	2.8448	0.0594	1.4599	1.4667	1.4633	11209.30	11233.30	1440.00	2107.15	28.2
130385	May-11	28-May-11	AM1	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7929	2.9104	0.1175	1.4502	1.4565	1.4534	11233.30	11257.30	1440.00	2092.82	56.1

Average (ug/m³)	34.2
Max (ug/m³)	56.1
Min (ug/m³)	21.7

Action Level (ug/m³)	146
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Tai Tung Pui Social Service Building (AM2) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM2
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130362	May-11	5-May-11	AM2	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7833	2.8772	0.0939	1.5064	1.4955	1.5010	5291.10	5315.10	1440.00	2161.37	43.4
130368	May-11	11-May-11	AM2	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.778	2.8163	0.0383	1.4847	1.4859	1.4853	5315.10	5339.10	1440.00	2138.83	17.9
130374	May-11	17-May-11	AM2	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.7727	2.8325	0.0598	1.5064	1.5024	1.5044	5339.10	5363.10	1440.00	2166.34	27.6
130380	May-11	23-May-11	AM2	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7903	2.8909	0.1006	1.5001	1.5070	1.5036	5363.10	5387.10	1440.00	2165.11	46.5
130386	May-11	28-May-11	AM2	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7905	2.9425	0.1520	1.4903	1.4967	1.4935	5387.10	5411.10	1440.00	2150.64	70.7

Average (ug/m³)	41.2
Max (ug/m³)	70.7
Min (ug/m³)	17.9

Action Level (ug/m³)	151
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Wu Siu Kui Primary School (AM3) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM3
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130363	May-11	5-May-11	AM3	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7809	2.9044	0.1235	1.4734	1.4638	1.4686	9457.39	9481.39	1440.00	2114.78	58.4
130369	May-11	11-May-11	AM3	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.7851	2.8393	0.0542	1.4545	1.4554	1.4550	9481.39	9505.39	1440.00	2095.13	25.9
130375	May-11	17-May-11	AM3	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.7707	2.8445	0.0738	1.4734	1.4699	1.4717	9505.39	9529.39	1440.00	2119.18	34.8
130381	May-11	23-May-11	AM3	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7942	2.8855	0.0913	1.4678	1.4739	1.4709	9529.39	9553.39	1440.00	2118.02	43.1
130387	May-11	28-May-11	AM3	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7836	2.9453	0.1617	1.4593	1.4649	1.4621	9553.39	9577.39	1440.00	2105.42	76.8

Average (ug/m³)	47.8
Max (ug/m³)	76.8
Min (ug/m³)	25.9

Action Level (ug/m³)	150
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Choi Cheung Kok Secondary School (AM4) - 24 hour TSP

Filter No.			Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM4
	Month	Date				Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130364	May-11	5-May-11	AM4	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7798	2.8852	0.1054	1.4772	1.4670	1.4721	10339.12	10363.12	1440.00	2119.82	49.7
130370	May-11	11-May-11	AM4	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.7889	2.8460	0.0571	1.4571	1.4581	1.4576	10363.12	10387.12	1440.00	2098.94	27.2
130376	May-11	17-May-11	AM4	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.782	2.8521	0.0701	1.4772	1.4735	1.4754	10387.12	10411.12	1440.00	2124.50	33.0
130382	May-11	23-May-11	AM4	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7848	2.9289	0.1441	1.4713	1.4778	1.4746	10411.12	10435.12	1440.00	2123.35	67.9
130388	May-11	28-May-11	AM4	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7835	2.8387	0.0552	1.4623	1.4682	1.4653	10435.12	10459.12	1440.00	2109.96	26.2

Average (ug/m³)	40.8
Max (ug/m³)	67.9
Min (ug/m³)	26.2
Action Level (ug/m³)	150
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Tuen Mun Town Hall (AM5) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time (mins.)	Total vol. (m³)	(ug/m³) AM5
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130365	May-11	5-May-11	AM5	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7832	2.8139	0.0307	1.4899	1.4791	1.4845	10125.27	10149.27	1440.00	2137.68	14.4
130371	May-11	11-May-11	AM5	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.7834	2.8459	0.0625	1.4686	1.4697	1.4692	10149.27	10173.27	1440.00	2115.58	29.5
130377	May-11	17-May-11	AM5	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.7740	2.8142	0.0402	1.4899	1.4860	1.4880	10173.27	10197.27	1440.00	2142.65	18.8
130383	May-11	23-May-11	AM5	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7804	2.8679	0.0875	1.4837	1.4905	1.4871	10197.27	10221.27	1440.00	2141.42	40.9
130389	May-11	28-May-11	AM5	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7839	2.8468	0.0629	1.4741	1.4803	1.4772	10221.27	10245.27	1440.00	2127.17	29.6




Average (ug/m³)	26.6
Max (ug/m³)	40.9
Min (ug/m³)	14.4
Action Level (ug/m³)	146
Limit Level (ug/m³)	260




Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Yan Oi Tong Community and Sports Centre (AM6) - 24 hour TSP




Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM6
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130366	May-11	5-May-11	AM6	Cloudy	Normal Operation	758.0	756.0	23.0	26.0	50.0	50.0	2.7901	2.8257	0.0356	1.4908	1.4813	1.4861	6458.80	6482.80	1440.00	2139.91	16.6
130372	May-11	11-May-11	AM6	Fine	Normal Operation	754.0	755.0	29.0	29.0	50.0	50.0	2.7808	2.8399	0.0591	1.4720	1.4730	1.4725	6482.80	6506.80	1440.00	2120.40	27.9
130378	May-11	17-May-11	AM6	Cloudy	Normal Operation	758.0	757.0	23.0	24.0	50.0	50.0	2.7802	2.8503	0.0701	1.4908	1.4873	1.4891	6506.80	6530.80	1440.00	2144.23	32.7
130384	May-11	23-May-11	AM6	Cloudy	Normal Operation	755.0	756.0	24.0	22.0	50.0	50.0	2.7903	2.8679	0.0776	1.4853	1.4913	1.4883	6530.80	6554.80	1440.00	2143.15	36.2
130390	May-11	28-May-11	AM6	Fine	Normal Operation	754.0	757.0	27.0	26.0	50.0	50.0	2.7798	2.8560	0.0762	1.4768	1.4823	1.4796	6554.80	6578.80	1440.00	2130.55	35.8




Average (ug/m³)	29.8
Max (ug/m³)	36.2
Min (ug/m³)	16.6

Action Level (ug/m³)	147
Limit Level (ug/m³)	260

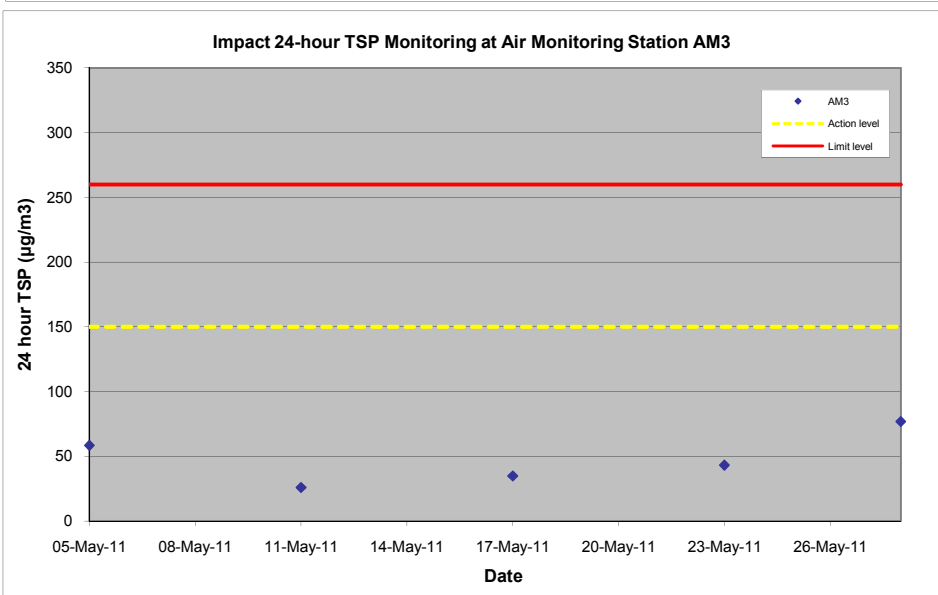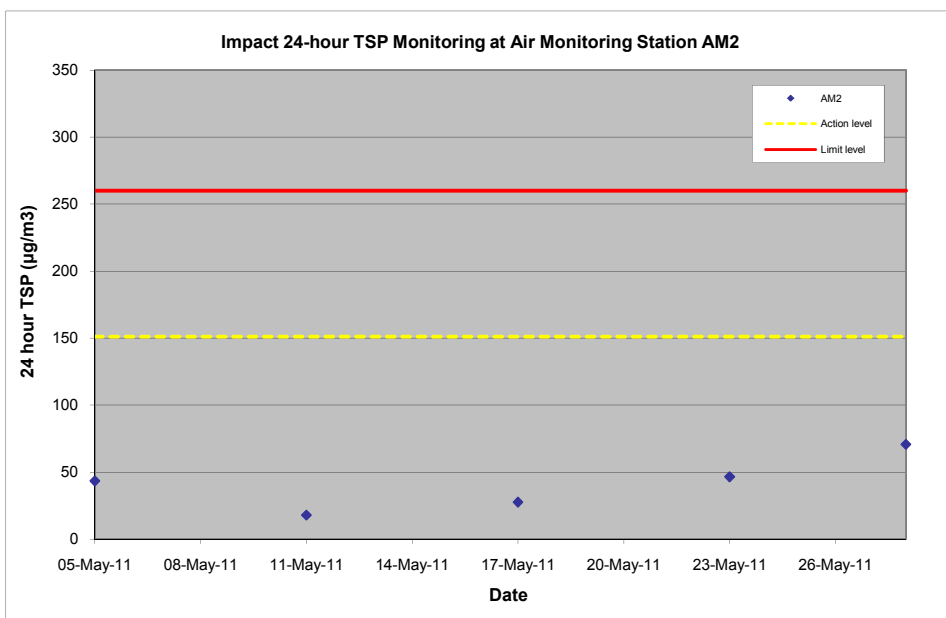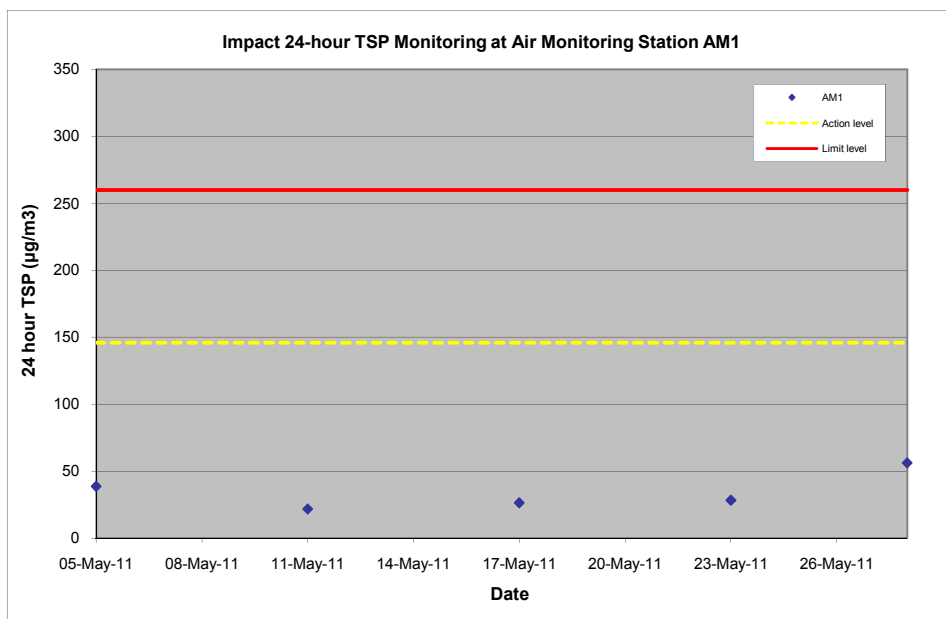

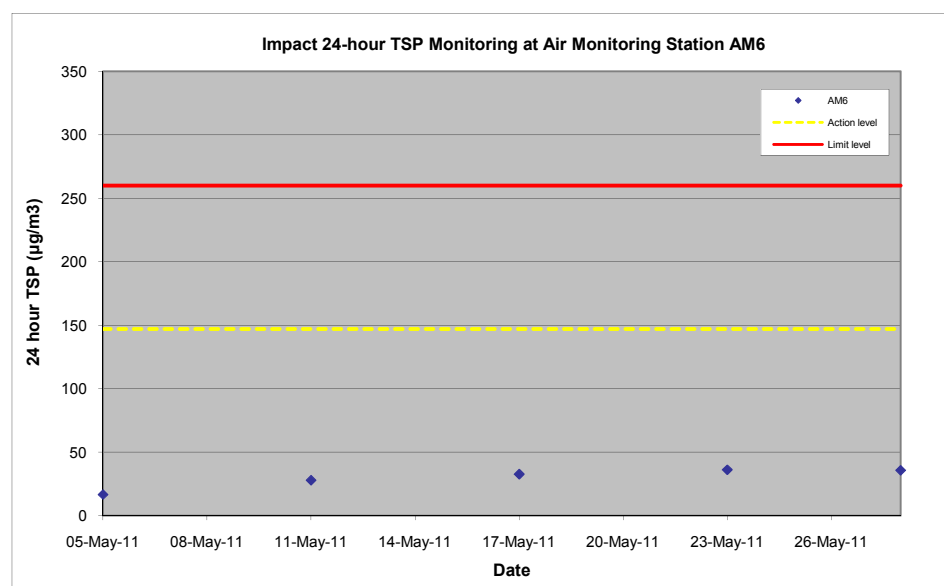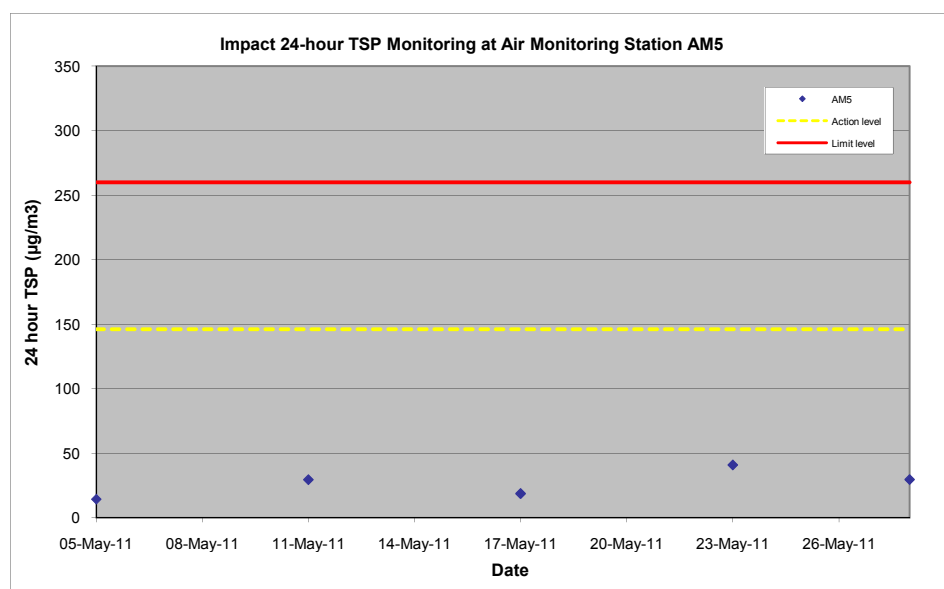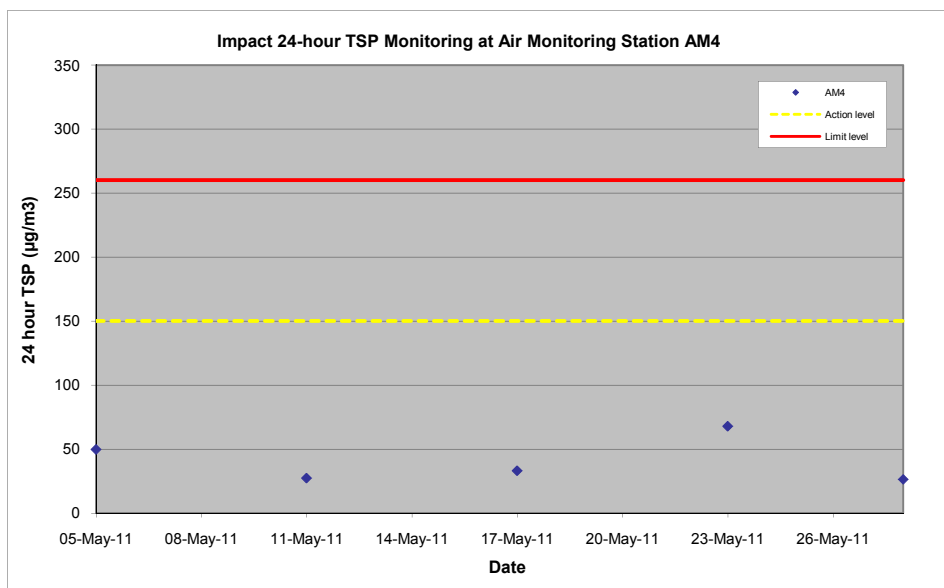

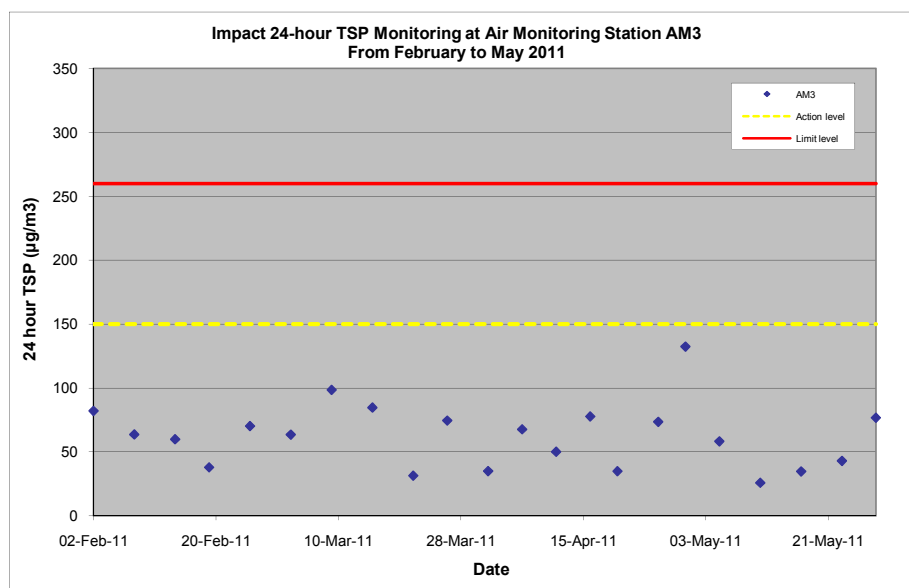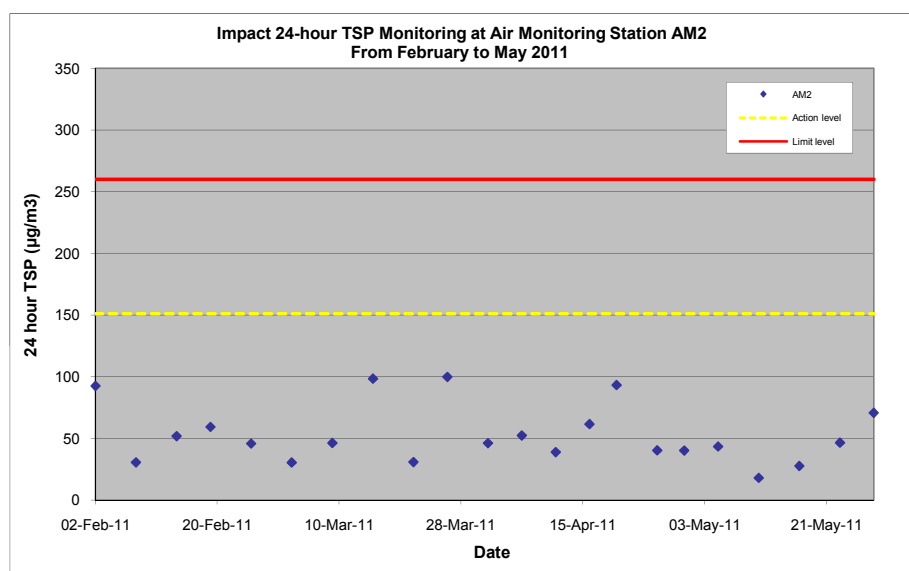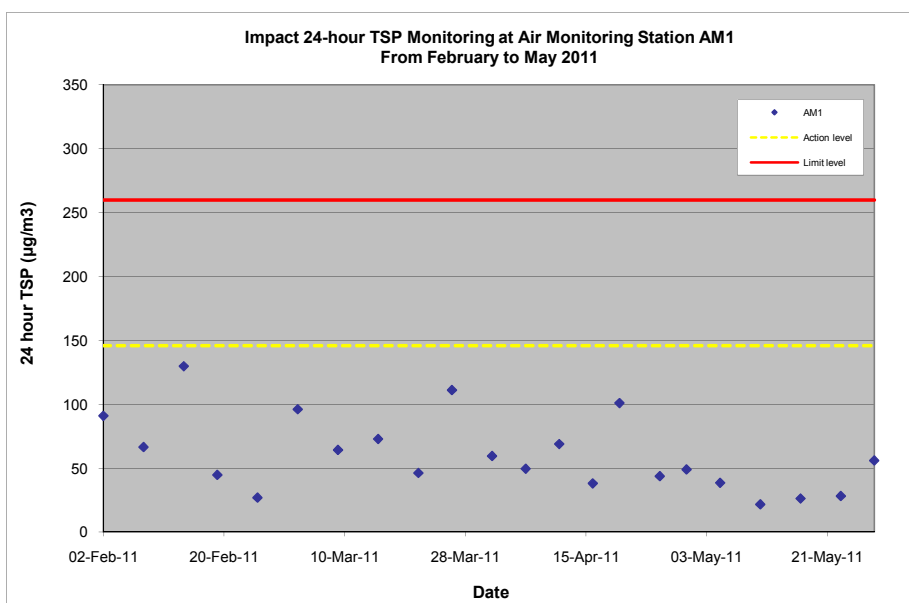


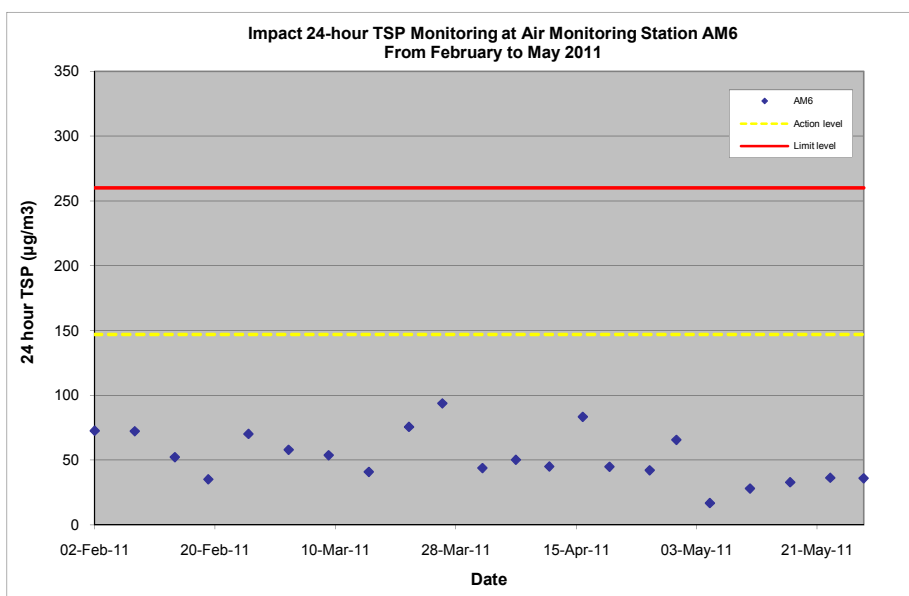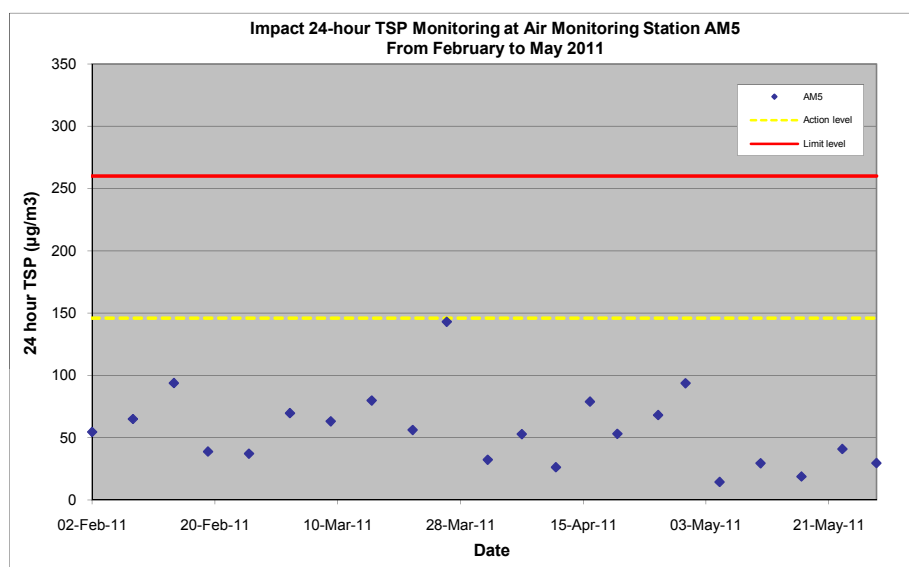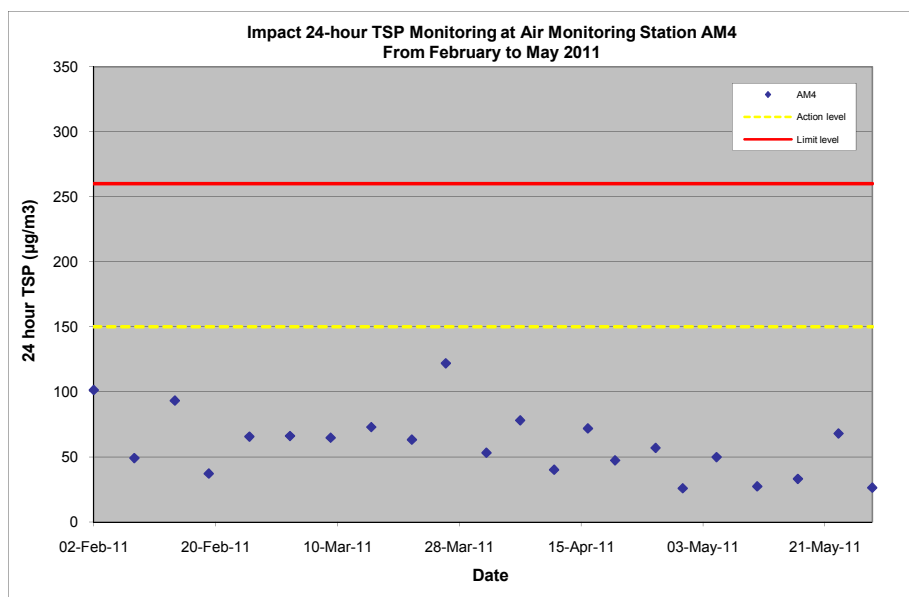






Appendix F

Wind Data

Wind Monitoring Data – Wind Speed during Air Quality Monitoring in May 2011

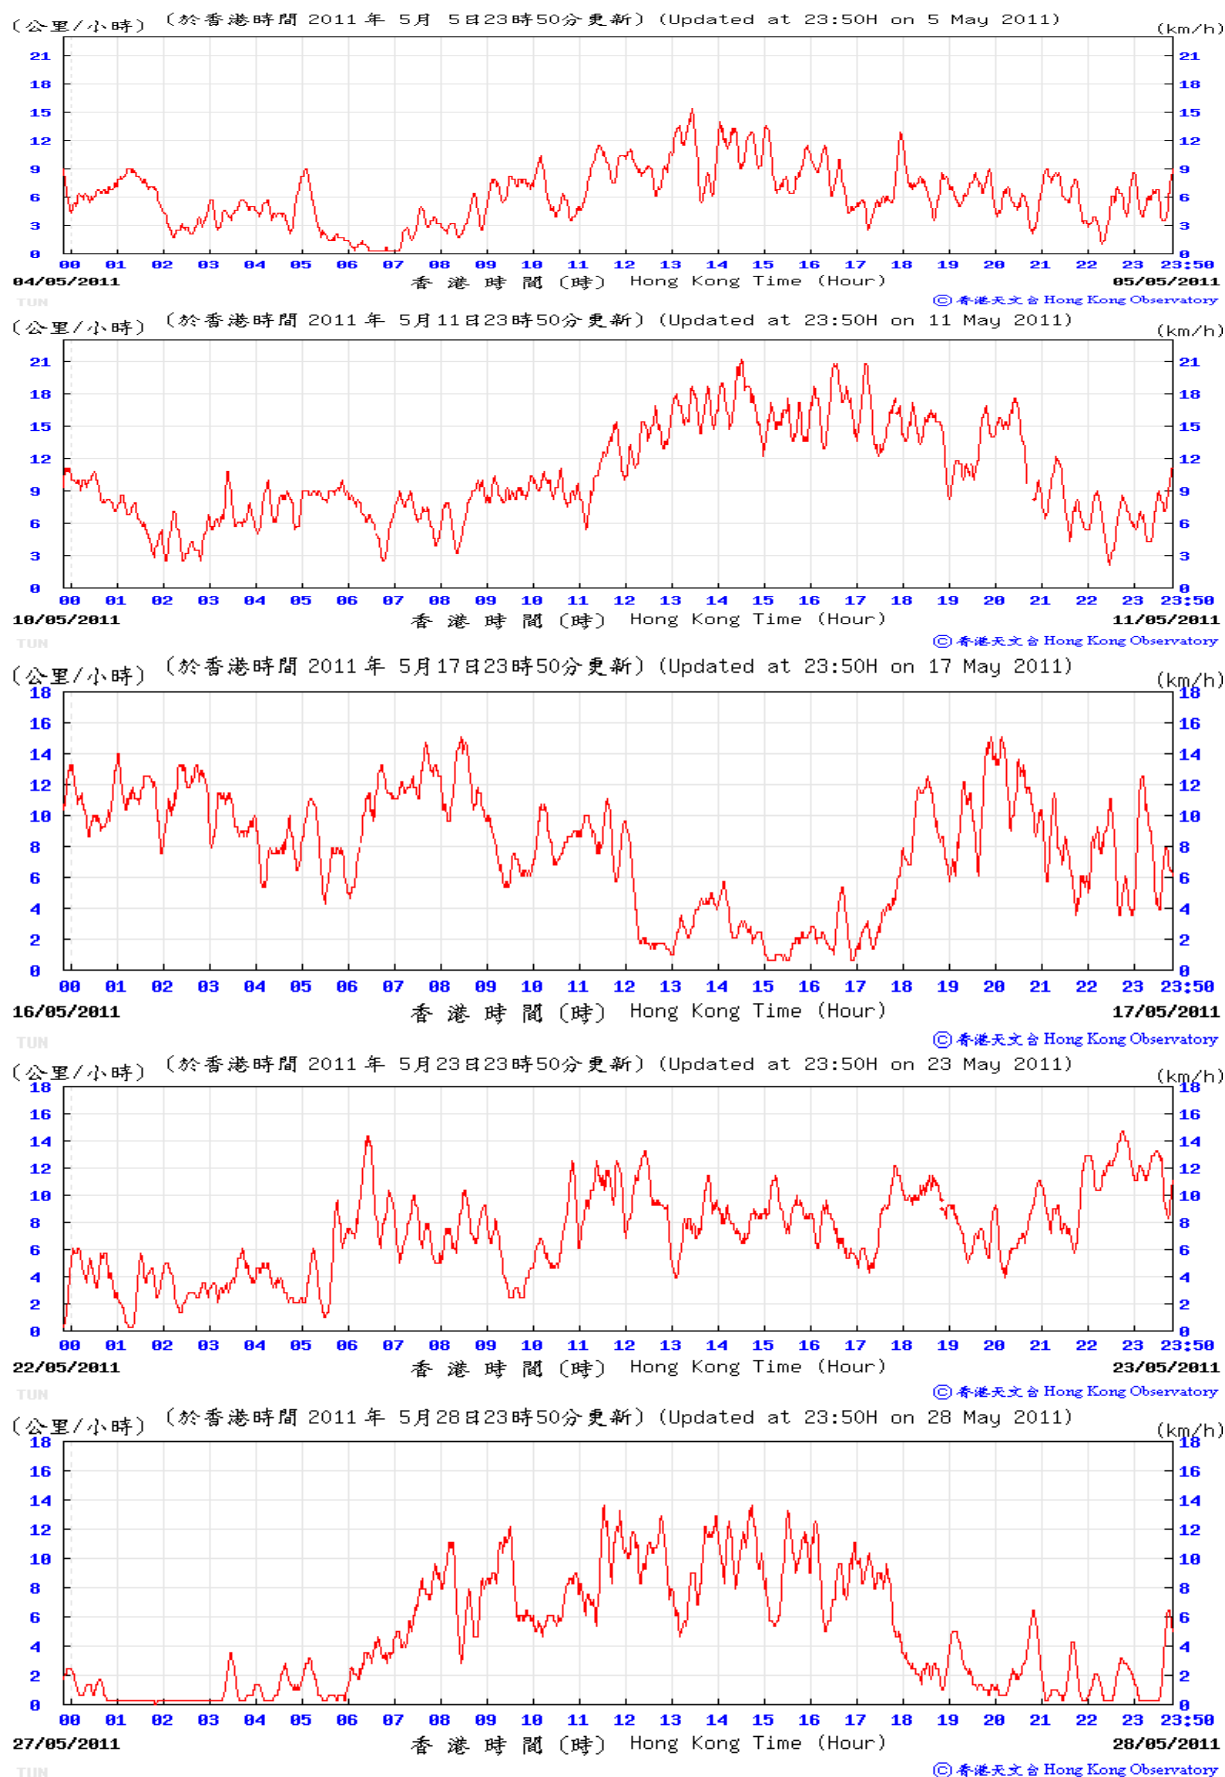

Wind Monitoring Data – Wind Direction during Air Quality Monitoring in May 2011

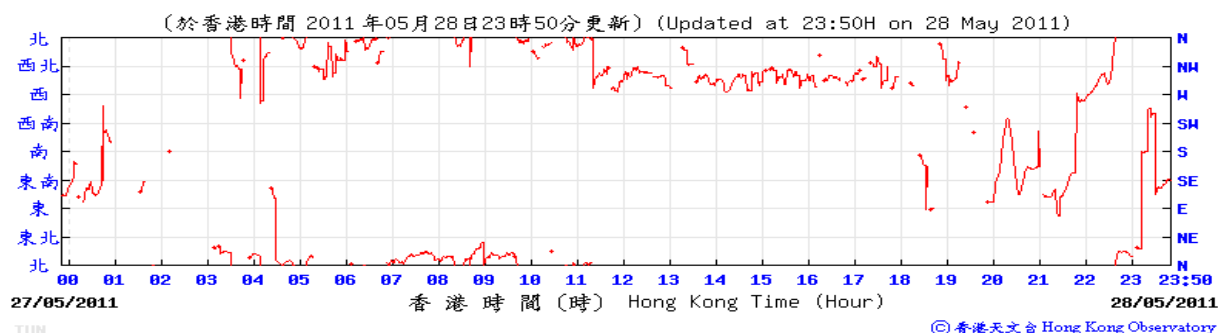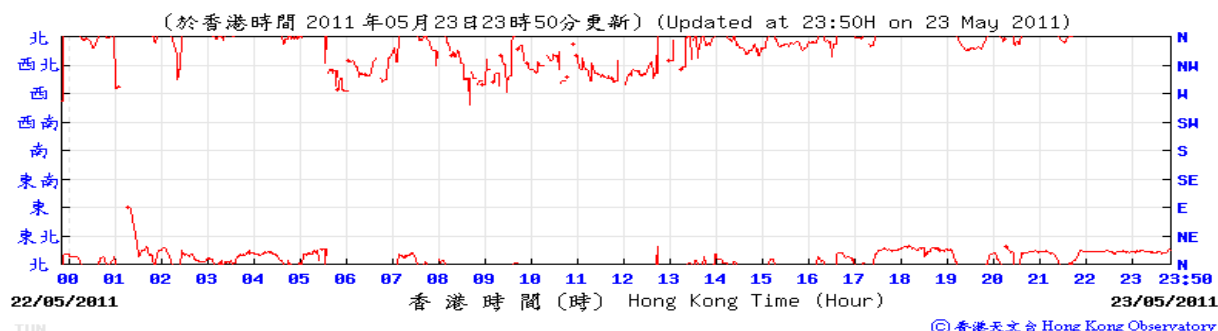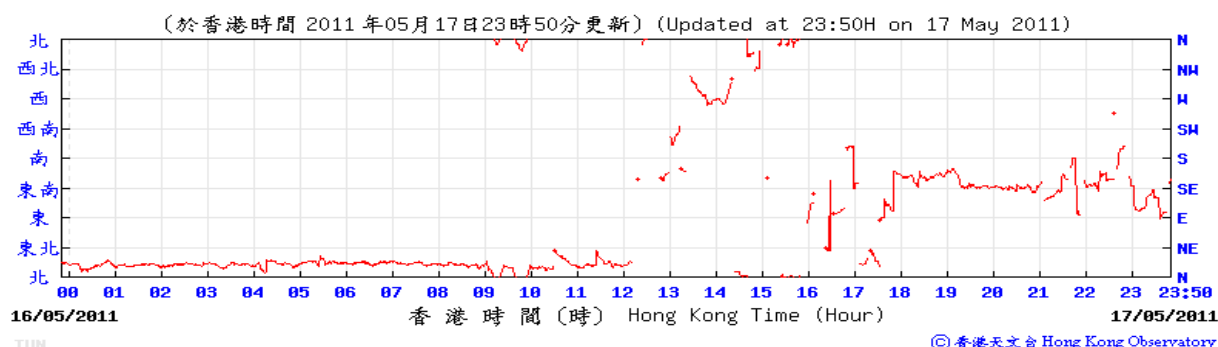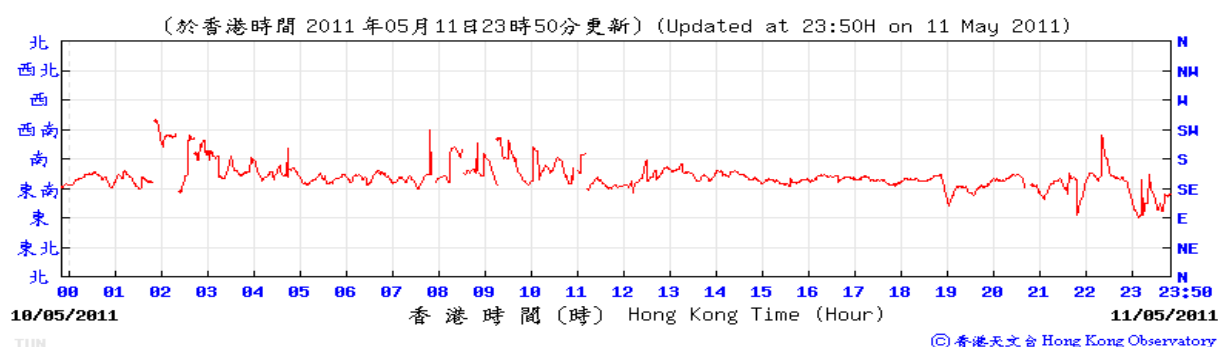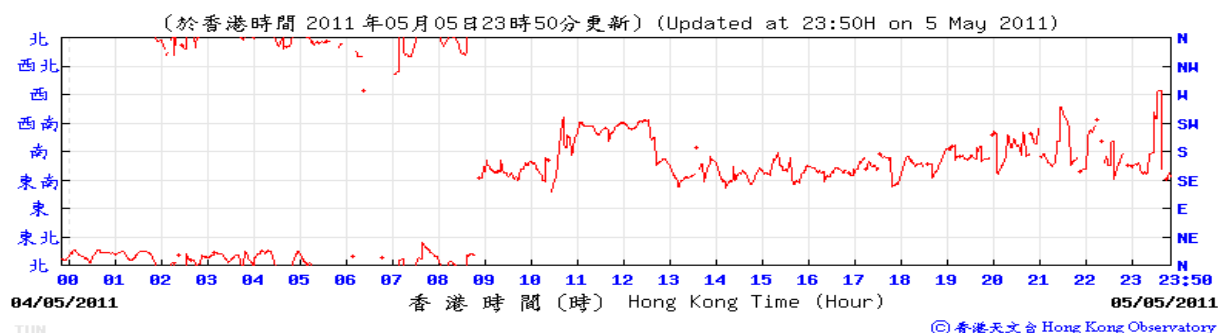

Appendix G

**Calibration Certificates
of Noise Monitoring
Equipments**

CERTIFICATE OF CALIBRATION

Issued by: Brüel & Kjær UK Ltd.

Date of Issue: 10 NOV 2009 Certificate Number: 17957



0174

Brüel & Kjær 

Bedford House, Rutherford Close, Stevenage.
Hertfordshire. SG1 2ND
Telephone: 01438 739100 Fax.: 01438 739199
E-Mail : ukservice@bksv.com

Page 1 of 4 pages

Approved signatory

Name: S. TILAHUN

Signature: 

CALIBRATION OF MULTI FREQUENCY CALIBRATOR TYPE 4226 ("Free Field and Random" version)

Client: ARUP ACOUSTICS
PARKIN HOUSE
8 ST THOMAS STREET, WINCHESTER
HANTS SO23 9HE

Calibrator Type 4226, S/No: 1531372

With Coupler UA0915, S/No: 1531372

Client Inventory Number: —

Manufacturer: Brüel & Kjær

Equipment Received on: 13 OCT 2009

Calibration Date: 10 NOV 2009

Brüel & Kjær Reference No: 1-192904717

Measurement Method

The Calibration was performed to Laboratory Procedure TWI-103.

Sound pressure level in the 1/2 inch coupler of the calibrator was measured with a laboratory grade condenser microphone Type 4180, used as a working standard, calibrated by the National Physical Laboratory.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to recognised national standards, and to units of measurement realised at the National Physical Laboratory or other recognised national standards laboratories. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957

Page 2 of 4 pages

The measured sound pressure was compared with that generated in the coupler of a working standard pistonphone calibrated by the National Physical Laboratory whose output was cross checked against a reference standard pistonphone, also calibrated by the National Physical Laboratory, using the same microphone and at the same ambient conditions. Appropriate corrections for atmospheric pressure conditions during calibration and for the measurement frequency and level response were taken into account.

Sound pressure level results are the mean of 5 measurements.

Results apply directly to the following settings on the calibrator, pressure, linear, calibration, 94dB, microphone group a, b, c.

Results for frequency and distortion are the result of a single measurement.

Results for 104 and 114dB are only at 125Hz, 1kHz and 8kHz, compared with the output at 94dB.

Calibration results apply at ambient conditions during the process of calibration.

Calibrations marked (Not UKAS Accredited) in this certificate have been included for completeness.

CALIBRATION RESULTS

4226 Settings: Linear, Pressure, 94dB, Microphone Group c.

Frequency Setting Hz	Sound Pressure Level in dB re 20µPa	Frequency Hz (Not UKAS Accredited)	Distortion % (Not UKAS Accredited)
31.5	94.15	31.63	0.5
63	94.13	63.13	0.2
125	94.09	125.9	0.1
250	94.06	251.3	0.1
500	94.04	502.5	0.1
1k	94.08	1.005k	0.1
2k	94.04	1.979k	0.3
4k	94.04	3.957k	0.7
8k	94.21	7.915k	0.2
12.5k	94.12	12.66k	0.2

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957

Page 3 of 4 pages

Expanded uncertainty of calibration:

Sound Pressure Level: $\pm 0.15\text{dB}$ from 31.5Hz to 2kHz,
 $\pm 0.20\text{dB}$ at 4kHz and 8kHz,
 $\pm 0.25\text{dB}$ at 12.5kHz
Frequency: ± 1 last significant digit reported.
Distortion: $\pm 0.3\%$ distortion.

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor $k=2$, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

ADDITIONAL TESTS

Sound Pressure Levels at Settings of 94, 104 and 114 dB

Frequency	Difference 104-94dB	Difference 114-94dB
125 Hz	9.99	19.97
1kHz	10.00	19.98
8kHz	9.96	19.94

Result of a single measurement, expanded uncertainty $\pm 0.15\text{dB}$

Inverted "A" Weighting, Readings Relative to 1kHz in dB

Frequency Hz	31.5	63	125	250	500	1 k	2 k	4 k	8 k	12.5 k
Target Value	+ 39.4	+ 26.2	+ 16.1	+ 8.6	+ 3.2	0	- 1.2	- 1.0	+ 1.1	+ 4.3
Reading	39.6	26.2	16.1	8.6	3.2	0.0	-1.2	-0.9	1.3	4.4

Target values according to BS EN 60651 - 1994 - results of a single measurement, values rounded to 0.1 dB, expanded uncertainty $\pm 0.3\text{dB}$.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957
Page 4 of 4 pages

Free Field and Random settings

	Free Field Setting						Random	
	Microphone Group a		Microphone Group b		Microphone Group c		Microphone Group b	
Freq. Hz	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB
250	0	0.00	0	0.00	0	0.00	0	0.00
500	0	0.00	0	0.00	0	0.00	0	0.00
1k	+0.15	0.14	+0.20	0.19	+0.10	0.08	+0.05	0.03
2k	+0.50	0.48	+0.45	0.43	+0.35	0.34	+0.10	0.08
4k	+1.35	1.33	+1.05	1.03	+0.95	0.93	+0.15	0.13
8k	+4.50	4.46	+2.80	2.77	+2.60	2.58	+0.40	0.38
12.5k	+7.35	7.28	+5.60	5.54	+5.05	5.00	+1.50	1.48

Target values as specified in the manufacturer's manual, result of a single measurement, expanded uncertainty $\pm 0.2\text{dB}$.

Ambient conditions during calibration were:

Atmospheric Pressure 100.7 kPa

Temperature 24 °C

Relative Humidity 47 %

Checked by:



Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010001

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320707
Brüel & Kjær ½ " Microphone Kit	4188	2630746

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010002

Tel: +852 2268 3216

Fax: +852 2268 3950


CERTIFICATE OF CONFORMITY


<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2654435
Brüel & Kjær ½ " Microphone Kit	4188	2658546

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature: 

Signature: 

Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372
Certificate of Calibration Serial No.	17957	
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009	
UKAS Accredited Calibration Laboratory No.	07174	

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010003

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320694
Brüel & Kjær ½ " Microphone Kit	4188	2641132

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAC Certificate No. 2010004

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2654436
Brüel & Kjær ½ " Microphone Kit	4188	2658547

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature: 

Signature: 

Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010005

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2562763
Brüel & Kjær ½ " Microphone Kit	4188	2658559

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAC Certificate No. 2010006

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320696
Brüel & Kjær ½ " Microphone Kit	4188	2630747

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test	
Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372
Certificate of Calibration Serial No.	17957	
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009	
UKAS Accredited Calibration Laboratory No.	07174	

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010021

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

Description of Test Instrument
RION NC-74 Acoustic Calibrator


Type No
NC-74


Serial No
34304660

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature: 

Signature: 

Ambient Conditions During Test	
Atmospheric Pressure:	1KPa
Air Temperature:	22°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference Calibrator

Type No

Serial No

Brüel & Kjær Multi Frequency Calibrator
Brüel & Kjær Coupler

4226
UA0915

1531372
1531372

Certificate of Calibration Serial No.

17957

By Brüel & Kjær (UK) Ltd Calibration Date:

10 November 2009

NAMAS Accredited Calibration Laboratory No.

07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Appendix H

**Impact Noise
Monitoring Results**

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 6 May 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:50 - 10:20	75	75	77	71	76	Measured ≤ Baseline
N2	Tai Tung Pui Social Service Building	10:35 - 11:05	76	75	78	72	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:20 - 11:50	69	70	72	67	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	67	70	68	65	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	72	75	74	70	70	68
N6	Choi Cheung kok Secondary School	14:00 - 14:30	71	70	73	68	69	66

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 12 May 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:35 - 10:05	78	75	80	75	76	73
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	78	75	81	75	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:15 - 11:45	68	70	70	66	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	67	70	69	65	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	71	75	73	70	70	65
N6	Choi Cheung kok Secondary School	13:50 - 14:20	71	70	72	68	69	64

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 18 May 2011


ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:40 - 10:20	77	75	79	73	76	68
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	76	75	78	73	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:10 - 11:40	68	70	69	66	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	66	70	68	65	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	72	75	73	69	70	66
N6	Choi Cheung kok Secondary School	13:45 - 14:15	71	70	72	67	69	65

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level


Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 24 May 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:50 - 10:20	74	75	76	71	76	Measured ≤ Baseline
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	76	75	78	74	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:05 - 11:35	67	70	69	66	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	64	70	67	63	67	Measured ≤ Baseline
N5	Tuen King Building	13:10 - 13:40	72	75	73	70	70	66
N6	Choi Cheung kok Secondary School	13:45 - 14:15	70	70	72	69	69	62


Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

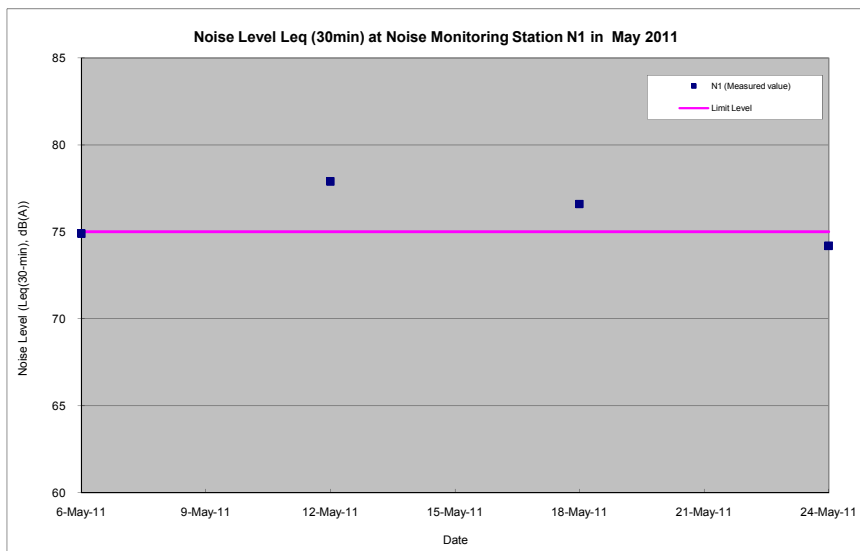


Note: For compliance comparison, please refer to above table and report.

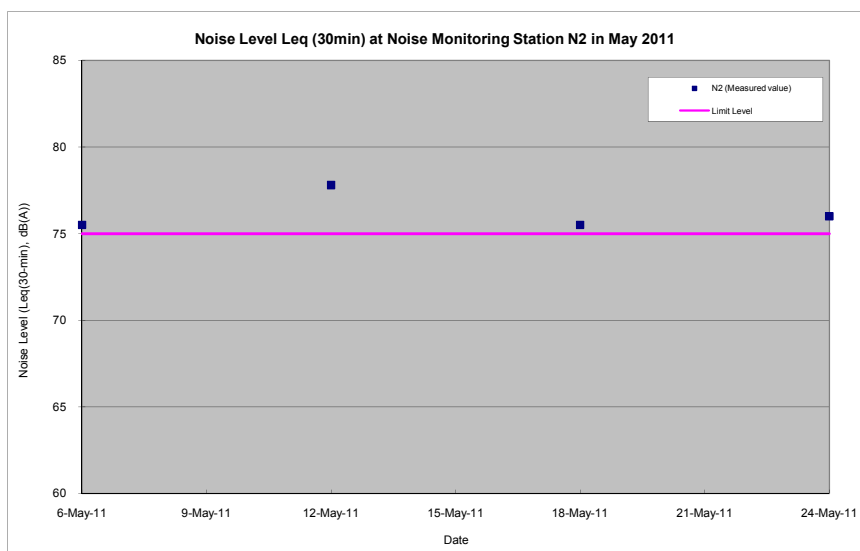


Note: For compliance comparison, please refer to above table and report.

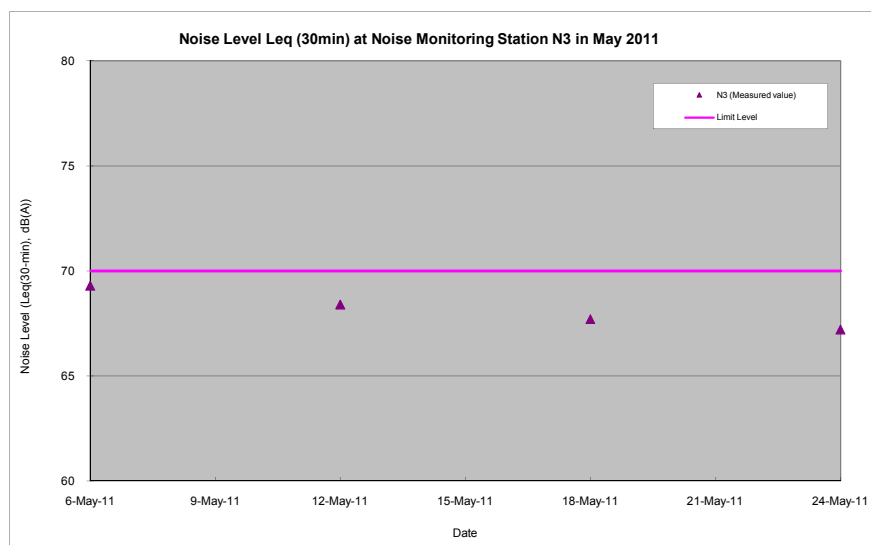


Note: For compliance comparison, please refer to above table and report.

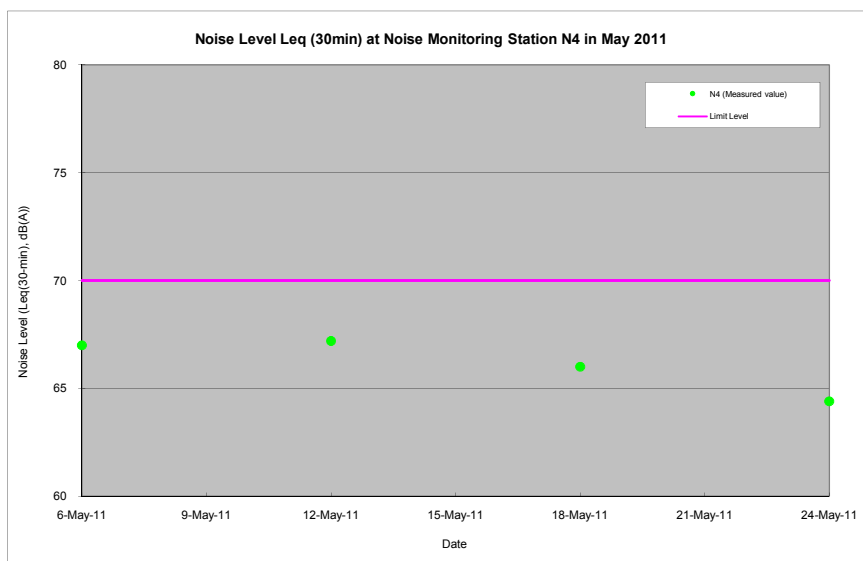


Note: For compliance comparison, please refer to above table and report.

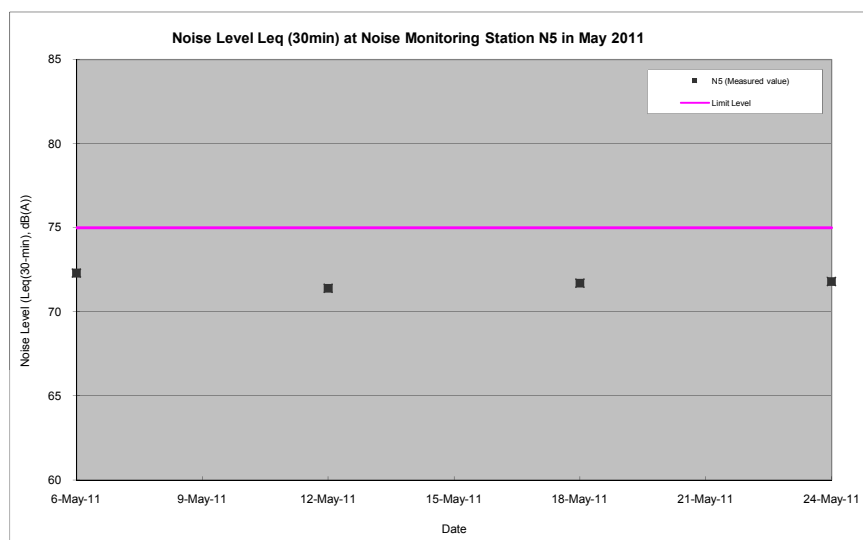


Note: For compliance comparison, please refer to above table and report.

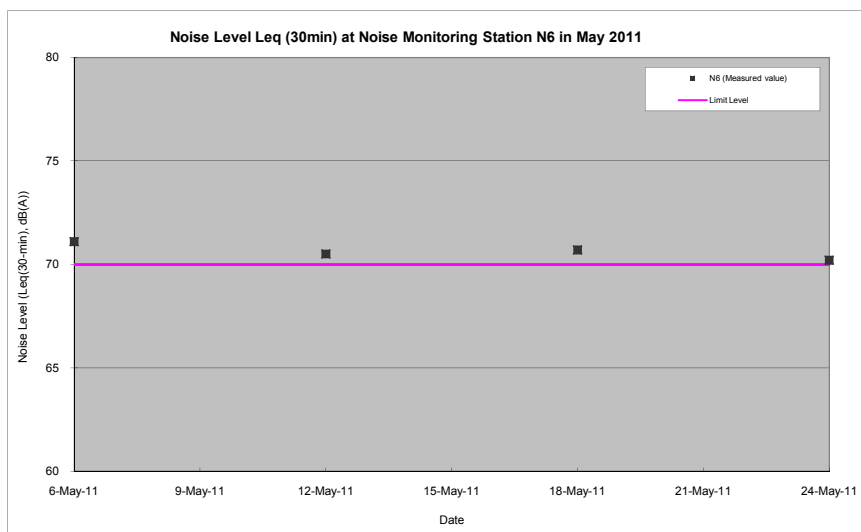


Note: For compliance comparison, please refer to above table and report.

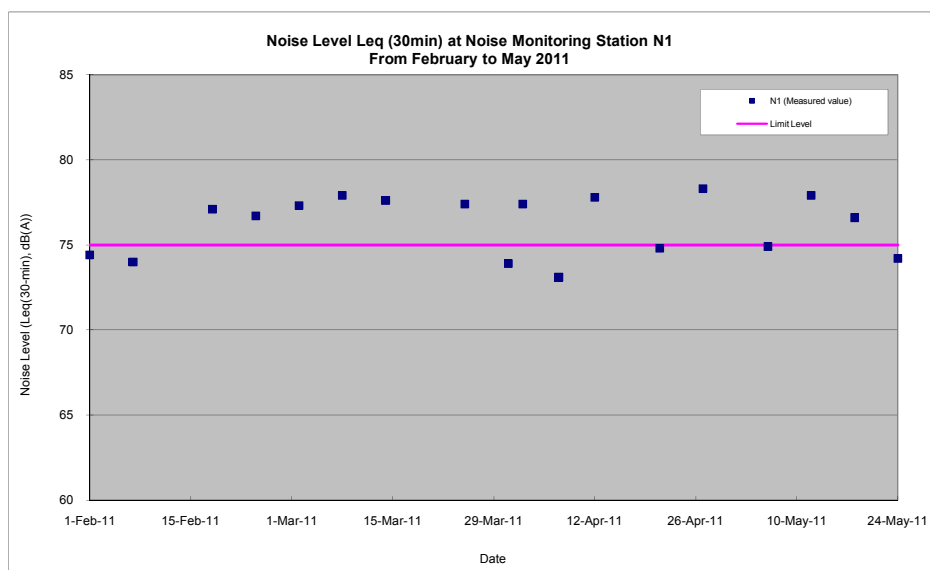


Note: For compliance comparison, please refer to above table and report.

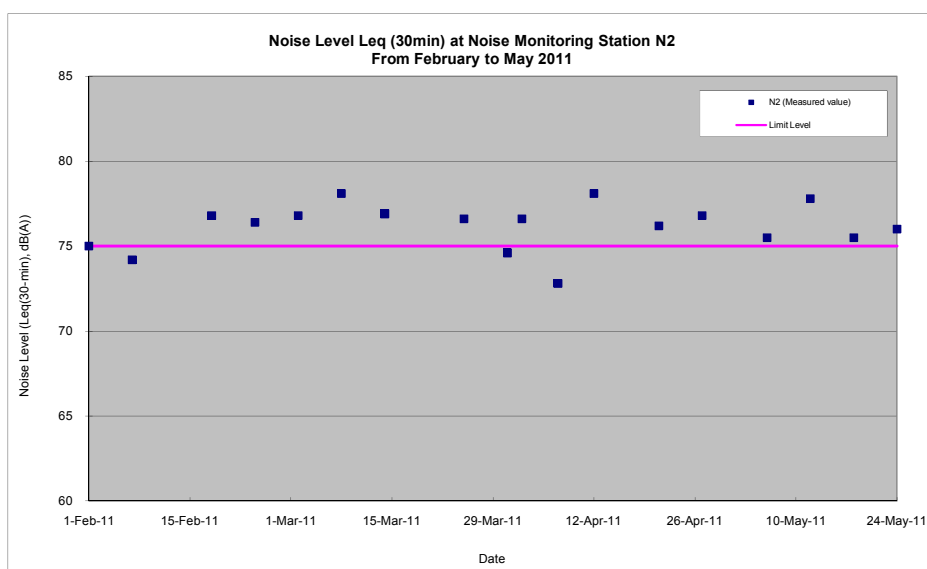


Note: For compliance comparison, please refer to above table and report.

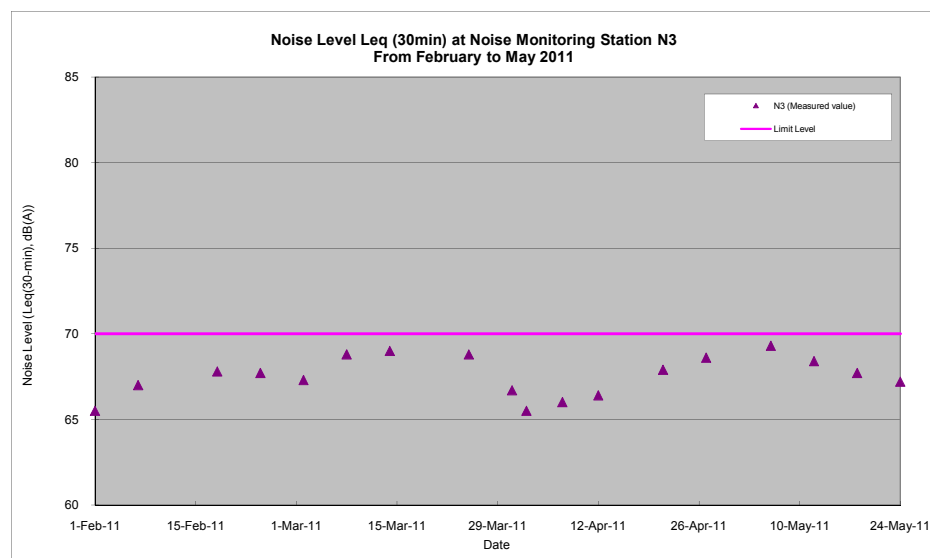


Note: For compliance comparison, please refer to above table and report.

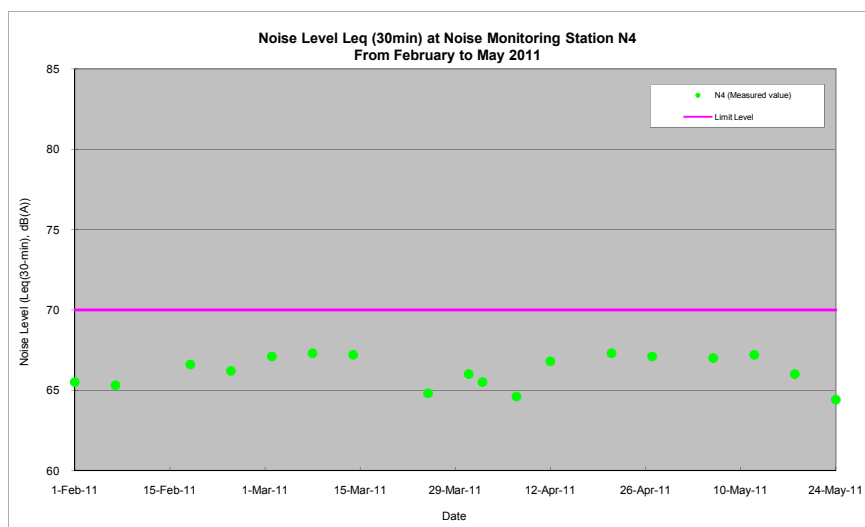

Note: For compliance comparison, please refer to above table and report.

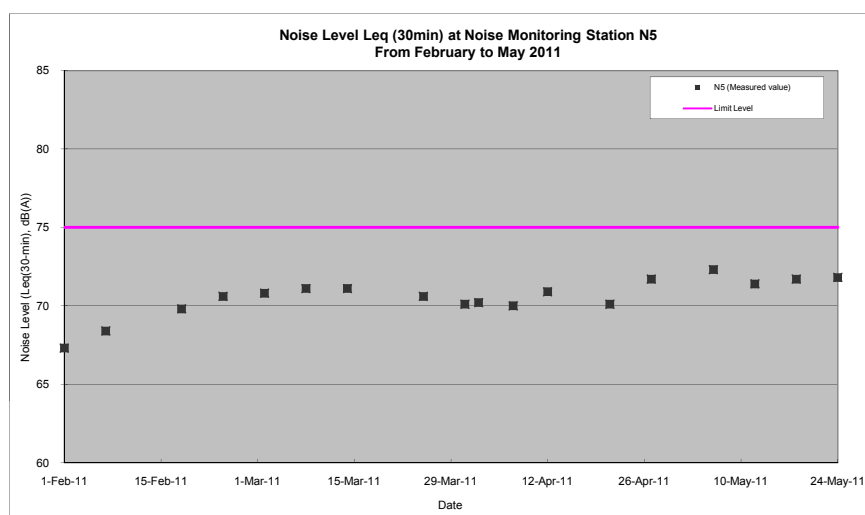

Note: For compliance comparison, please refer to above table and report.

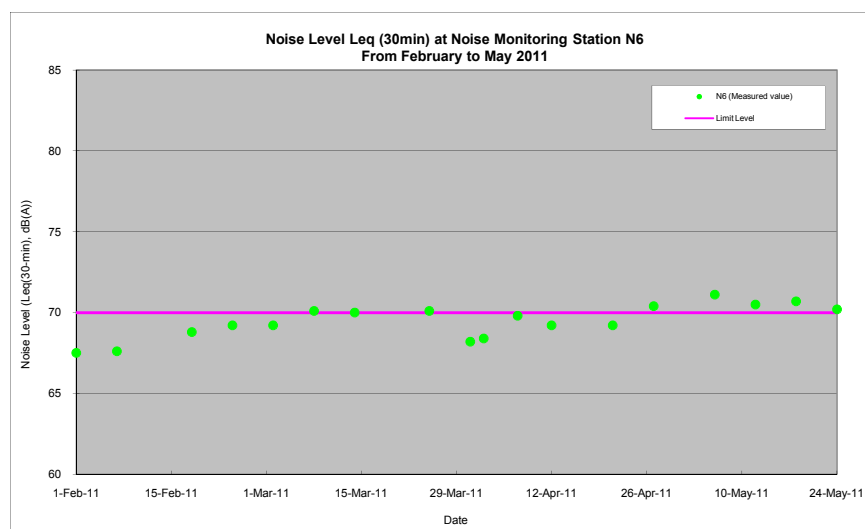

Note: For compliance comparison, please refer to above table and report.

Appendix I

**Landscape Summary
Report**

Total Tree No.	No of Contract	Numbers of Contract Tree + UTRA No.1
	Transplant	Transplant
	362	389
	Fell & Re.	Fell & Remove
	501	521
	Retain	Retain
	134	102
	Missing	Missing
	0	9

Unnamed
Dead Tree (Removed)
In Progress
Completed
Total
Completed (%)

Fell & Remove Status	Crown Pruning	1st Root Pruning	2nd Root Pruning	3rd Root Pruning & Transplant
157				
9 (On Ting E.)				
43	30	37	49	71
478	359	352	340	318
521	389	389	389	389
92%	92%	90%	87%	82%

Item	Drawing No.	Tree No.	Chinese Name	Location	Rec., In Contract Document	Recommendation	Fell & Remove	Crown Pruning	1st Root Pruning	2nd Root Pruning	3rd Root Pruning & Transplant	Remarks
1	6106	TW0001	石栗	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	08-Apr-11	11-Apr-11	12-May-11	Not Yet	
2	6106	TW0002	石栗	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	08-Apr-11	11-Apr-11	12-May-11	Not Yet	
3	6106	TW0003	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	07-Apr-11	24-Dec-10	16-Feb-11	07-Apr-11	Transplanted
4	6106	TW0004	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	11-Apr-11	24-Dec-10	16-Feb-11	11-Apr-11	Transplanted
5	6106	TW0012	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
6	6106	TW0013	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
7	6106	TW0014	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
8	6106	TW0015	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
9	6106	TW0016	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
10	6106	TW0021	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
11	6106	TW0022	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	11-Apr-11	29-Dec-10	17-Feb-11	11-Apr-11	Transplanted
12	6106	TW0023	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
13	6106	TW0024	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
14	6106	TW0025	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
15	6106	TW0026	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
16	6106	TW0030	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
17	6106	TW0033	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
18	6106	TW0034	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
19	6106	TW0035	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
20	6106	TW0036	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
21	6106	TW0037	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
22	6106	TW0040	-	Tuen Mun Road near Kam Fai Garden	Retain	-	-	-	-	-	-	
23	6106	TW0043	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
24	6106	TW0044	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	31-Dec-10	17-Feb-11	13-Apr-11	Transplanted
25	6106	TW0045	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	12-Apr-11	31-Dec-10	18-Feb-11	12-Apr-11	Transplanted
26	6106	TW0046	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	12-Apr-11	12-Jan-11	18-Feb-11	12-Apr-11	Transplanted
27	6106	TW0047	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
28	6106	TW0049	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
29	6106	TW0050	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
30	6106	TW0054	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
31	6106	TW0055	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Apr-11	-	-	-	-	
32	6106	TW0056	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
33	6106	TW0057	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
34	6106	TW0058	雙翼豆	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	

35	6106	TW0061	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
36	6106	TW0062	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
37	6106	TW0066	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
38	6106	TW0071	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
39	6106	TW0072	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
40	6106	TW0073	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
41	6106	TW0074	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	13-Jan-11	18-Feb-11	13-Apr-11	Transplanted
42	6106	TW0075	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	13-Jan-11	18-Feb-11	13-Apr-11	Transplanted
43	6106	TW0076	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
44	6106	TW0079	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
45	6106	TW0080	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
46	6106	TW0081	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
47	6106	TW0082	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
48	6106	TW0083	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
49	6106	TW0088	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
50	6106	TW0089	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
51	6106	TW0090	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
52	6106	TW0093	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
53	6106	TW0095	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
54	6106	TW0096	死樹	Tuen Mun Road near Kam Fai Garden	Remove	Remove	-	-	-	-	-	
55	6106	TW0097	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
56	6106	TW0102	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
57	6106	TW0104	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
58	6106	TW0106	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
59	6106	TW0107	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
60	6106	TW0108	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
61	6106	TW0112	木麻黃	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
62	6106	TW0113	山指甲	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
63	6106	TW0114	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
64	6106	TW0115	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
65	6106	TW0116	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
66	6106	TW0117	木麻黃	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
67	6106	TW0118	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
68	6106	TW0119	木麻黃	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
69	6106	TW0120	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
70	6106	TW0121	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
71	6106	TW0122	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
72	6106	TW0123	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
73	6106	TW0124	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
74	6106	TW0125	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
75	6106	TW0126	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
76	6106	TW0127	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
77	6106	TW0128	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
78	6106	TW0130	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
79	6106	TW0131	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
80	6106	TW0132	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
81	6106	TW0133	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
82	6106	TW0134	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
83	6106	TW0135	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
84	6106	TW0136	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
85	6106	TW0137	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	

86	6106	TW0138	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
87	6106	TW0139	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
88	6106	TW0140	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
89	6106	TW0141	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
90	6106	TW0142	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
91	6106	TW0143	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
92	6106	TW0144	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
93	6106	TW0145	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
94	6106	TW0146	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
95	6106	TW0147	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
96	6106	TW0148	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
97	6106	TW0149	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
98	6106	TW0150	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
99	6106	TW0151	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
100	6106	TW0152	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
101	6106	TW0153	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
102	6106	TW0154	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
103	6106	TW0155	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
104	6106	TW0156	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
105	6106	TW0157	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
106	6106	TW0158	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
107	6106	TW0159	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
108	6106	TW0160	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
109	6106	TW0161	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
110	6106	TW0162	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
111	6106	TW0163	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
112	6106	TW0165	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
113	6106	TW0166	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
114	6106	TW0167	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
115	6106	TW0168	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
116	6106	TW0169	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
117	6106	TW0170	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
118	6106	TW0171	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
119	6106	TW0172	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
120	6106	TW0173	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
121	6106	TW0174	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
122	6106	TW0175	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
123	6106	TW0176	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
124	6106	TW0177	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
125	6106	TW0178	銀合歡	Tuen Mun Road near Kam Fai Garden	Remove	Remove	13-Aug-10	-	-	-	-	
126	6106	TW0179	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
127	6106	TW0180	垂葉榕	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	03-Apr-11	03-Apr-11	03-Apr-11	03-Apr-11	Transplanted
128	6106	TW0181	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
129	6106	TW0182	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
130	6106	TW0183	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
131	6106	TW0185	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
132	6106	TW0186	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
133	6106	TW0187	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
134	6106	TW0188	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
135	6106	TW0189	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
136	6106	TW0190	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	

137	6106	TW0191	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
138	6106	TW0192	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
139	6106	TW0193	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
140	6106	TW0194	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
141	6106	TW0195	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
142	6106	TW0196	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
143	6106	TW0197	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
144	6106	TW0198	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
145	6106	TW0199	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
146	6106	TW0200	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
147	6105	TW0580	宮粉羊蹄甲	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	30-Oct-10	01-Nov-10	Transplanted
148	6105	TW0581	大葉合歡	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	06-Sep-10	24-Sep-10	Not Yet	Not Yet	
149	6105	TW0582	死樹	Wong Chu Road near Ting Fuk House	Remove	Remove	29-May-10	-	-	-	-	Ref. letter 115
150	6105	TW0583	菩提樹	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
151	6105	TW0584	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
152	6105	TW0585	菩提樹	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
153	6105	TW0586	宮粉羊蹄甲	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Sep-10	08-Sep-10	30-Oct-10	01-Nov-10	Transplanted
154	6105	TW0587	-	Wong Chu Road near Ting Fuk House	Transplant	Missing	20-Jan-11	-	-	-	-	Poor Health
155	6104	TW0588	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Transplant	20-Jan-11	-	-	-	-	Poor Health
156	6104	TW0589	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
157	6104	TW0590	朴樹	Wong Chu Road near Ting Fuk House	Fell	Fell	29-May-10	-	-	-	-	
158	6104	TW0591	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	10-Aug-10	24-Sep-10	30-Oct-10	Transplanted
159	6104	TW0592	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	30-Oct-10	Transplanted
160	6104	TW0593	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10		-	-	-	Ref. letter 115
161	6104	TW0594	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	11-Oct-10	Transplanted
162	6104	TW0595	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	29-Oct-10	Transplanted
163	6104	TW0596	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	10-Aug-10	22-Sep-10	11-Oct-10	Transplanted
164	6104	TW0597	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
165	6104	TW0598	-	Wong Chu Road near Ting Fuk House	Fell	-	29-May-10	-	-	-	-	
166	6104	TW0599	-	Wong Chu Road near Ting Fuk House	Fell	-	29-May-10	-	-	-	-	
167	6104	TW0600	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	11-Oct-10	Transplanted
168	6104	TW0601	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Transplant	20-Jan-11	-	-	-	-	Poor Health
169	6104	TW0603	石栗	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	05-Mar-11	06-Apr-11	Not Yet	
170	6104	TW0604	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
171	6104	TW0605	石栗	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	05-Mar-11	06-Apr-11	Not Yet	
172	6104	TW0606	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
173	6104	TW0607	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
174	6104	TW0608	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	02-Jun-11	Not Yet	Not Yet	Not Yet	
175	6104	TW0609	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	02-Jun-11	02-Jun-11	Not Yet	Not Yet	
176	6104	TW0610	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	31-May-11	02-Jun-11	Not Yet	Not Yet	
177	6104	TW0611	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	22-Sep-10	22-Sep-10	02-Nov-10	Not Yet	
178	6104	TW0612	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	31-May-11	02-Jun-11	Not Yet	Not Yet	
179	6104	TW0613	銀合歡	Tuen Mun Road near Ting Fuk House	Remove	Remove	29-Aug-10	-	-	-	-	
180	6104	TW0614	細葉榕	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	31-May-11	02-Jun-11	Not Yet	Not Yet	10/9/2010
181	6104	TW0615	細葉榕	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	02-Jun-11	Not Yet	Not Yet	Not Yet	10/9/2010
182	6104	TW0616	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	28-Sep-10	16-Nov-10	18-Nov-10	Transplanted
183	6104	TW0617	鳳凰木	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	16-Sep-10	02-Nov-10	18-Nov-10	Transplanted
184	6104	TW0618	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	30-Sep-10	16-Nov-10	17-Nov-10	Transplanted
185	6104	TW0619	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	30-Sep-10	16-Nov-10	17-Nov-10	Transplanted
186	6104	TW0620	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
187	6104	TW0621	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	

188	6104	TW0622	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
189	6104	TW0623	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
190	6104	TW0624	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
191	6104	TW0625	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
192	6104	TW0626	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
193	6104	TW0627	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
194	6104	TW0628	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
195	6104	TW0629	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
196	6104	TW0630	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
197	6104	TW0631	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
198	6104	TW0632	-	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Missing	-	-	-	-	-	
199	6104	TW0633	雙翼豆	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	29-Sep-10	29-Sep-10	15-Nov-10	19-Nov-10	Transplanted
200	6104	TW0634	雙翼豆	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	18-Dec-10	28-Sep-10	29-Sep-10	15-Nov-10	-	Rootball size = 0.5m
201	6104	TW0635	石栗	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
202	6104	TW0636	銀合歡	Tuen Mun Road near Luk Cheung Kwong College	Remove	Remove	05-Sep-10	-	-	-	-	
203	6104	TW0637	黃花夾竹桃	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	02-Nov-10	09-Nov-10	Transplanted
204	6104	TW0638	黃花夾竹桃	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
205	6104	TW0639	台灣相思	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-May-10	-	-	-	-	Ref. letter 115
206	6104	TW0640	石栗	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
207	6104	TW0641	-	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	-	-	-	-	-	-	
208	6104	TW0642	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
209	6104	TW0643	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
210	6104	TW0644	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
211	6104	TW0645	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
212	6104	TW0646	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
213	6104	TW0647	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
214	6104	TW0677	大葉合歡	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
215	6104	TW0678	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
216	6104	TW0679	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
217	6103	TW0680	-	Tuen Mun Road Slip Road to Tuen Hing Road	Remove	-	-	-	-	-	-	
218	6103	TW0681	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
219	6103	TW0682	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
220	6103	TW0683	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
221	6103	TW0684	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
222	6103	TW0685	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
223	6103	TW0686	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
224	6103	TW0687	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
225	6103	TW0688	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
226	6103	TW0689	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
227	6103	TW0690	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
228	6103	TW0691	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
229	6103	TW0692	-	Tuen Mun Road Slip Road to Tuen Hing Road	Remove	-	-	-	-	-	-	
230	6103	TW0693	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
231	6103	TW0694	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
232	6103	TW0695	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
233	6103	TW0696	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
234	6103	TW0697	大葉合歡	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
235	6103	TW0698	宮粉羊蹄甲	Tuen Hi Road near Tuen Mun Road (YL/B)	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
236	6103	TW0699	宮粉羊蹄甲	Tuen Hi Road near Tuen Mun Road (YL/B)	Retain	Retain	-	-	-	-	-	
237	6103	TW0700	黃葛樹	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
238	6103	TW0701	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work

239	6103	TW0702	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
240	6103	TW0703	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
241	6103	TW0704	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
242	6103	TW0705	白千層	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
243	6103	TW0706	黃葛樹	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
244	6102	TW0707	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
245	6102	TW0708	-	Tuen Fat Road near Tuen Yan Street	Fell	-	08-Oct-10	-	-	-	-	Night Work
246	6102	TW0709	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
247	6102	TW0710	黃葛樹	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
248	6102	TW0711	鳳凰木	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
249	6102	TW0712	白千層	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
250	6102	TW0713	白千層	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
251	6102	TW0714	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
252	6102	TW0715	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
253	6102	TW0716	鳳凰木	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
254	6102	TW0717	木棉	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
255	6102	TW0718	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
256	6101	TW0719	白千層	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
257	6101	TW0720	白千層	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
258	6101	TW0722	大葉桉	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
259	6102	TW0723	-	Centre Median near Tuen Yan Street	Fell	-	-	-	-	-	-	Missing
260	6102	TW0724	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
261	6102	TW0725	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
262	6102	TW0726	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
263	6102	TW0727	假檳榔	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
264	6102	TW0728	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
265	6102	TW0729	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
266	6102	TW0730	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
267	6102	TW0731	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
268	6102	TW0732	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
269	6102	TW0733	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
270	6102	TW0734	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
271	6102	TW0735	石栗	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
272	6102	TW0736	木棉	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
273	6102	TW0737	石栗	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
274	6102	TW0738	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
275	6102	TW0739	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
276	6102	TW0740	黃葛樹	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
277	6102	TW0741	石栗	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
278	6102	TW0742	石栗	Centre Median near Tuen Yan Street	Fell	Fell	14-Oct-10	-	-	-	-	Night Work
279	6102	TW0743	黃葛樹	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
280	6102	TW0744	石栗	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
281	6102	TW0745	石栗	Centre Median near Tuen Yan Street	Fell	Fell	14-Oct-10	-	-	-	-	Night Work
282	6102	TW0746	石栗	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
283	6102	TW0747	白千層	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
284	6103	TW0748	石栗	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
285	6103	TW0749	白千層	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
286	6103	TW0750	鳳凰木	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
287	6103	TW0751	黃葛樹	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
288	6103	TW0752	鳳凰木	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	14-Oct-10	-	-	-	-	Night Work
289	6103	TW0753	黃葛樹	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	14-Oct-10	-	-	-	-	Night Work

[illegible]

341	6103	TW0805	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
342	6104	TW0806	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
343	6104	TW0807	木麻黃	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
344	6104	TW0808	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
345	6104	TW0809	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
346	6104	TW0810	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
347	6104	TW0811	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
348	6104	TW0812	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
349	6104	TW0813	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
350	6104	TW0814	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
351	6104	TW0815	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
352	6104	TW0816	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
353	6104	TW0817	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
354	6104	TW0818	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
355	6104	TW0819	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
356	6104	TW0820	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	
357	6104	TW0821	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
358	6104	TW0822	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
359	6104	TW0823	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
360	6104	TW0824	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
361	6104	TW0825	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
362	6104	TW0826	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
363	6104	TW0827	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
364	6104	TW0828	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
365	6104	TW0829	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
366	6104	TW0830	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
367	6104	TW0831	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
368	6103	TW0832	大葉合歡	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
369	6103	TW0833	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
370	6103	TW0834	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
371	6103	TW0835	大葉合歡	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
372	6103	TW0836	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
373	6103	TW0837	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
374	6103	TW0838	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
375	6103	TW0839	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
376	6103	TW0840	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
377	6103	TW0841	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
378	6103	TW0842	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
379	6103	TW0843	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	07-Sep-10	-	-	-	-	by other
380	6103	TW0844	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
381	6103	TW0845	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
382	6103	TW0846	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	07-Sep-10	-	-	-	-	by other
383	6103	TW0847	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	
384	6103	TW0848	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	23-Nov-10	-	-	-	-	Night Work
385	6103	TW0849	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	23-Nov-10	-	-	-	-	Night Work
386	6103	TW0851	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	23-Nov-10	-	-	-	-	Night Work
387	6103	TW0852	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	
388	6103	TW0853	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
389	6103	TW0854	桑	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	23-Nov-10	-	-	-	-	Night Work
390	6103	TW0855	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
391	6103	TW0856	-	Tuen Hi Road near Tuen Wui Street	Fell	-	-	-	-	-	-	Missing

392	6103	TW0857	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
393	6103	TW0858	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
394	6103	TW0859	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
395	6103	TW0860	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
396	6103	TW0861	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
397	6103	TW0862	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
398	6103	TW0863	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
399	6103	TW0864	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
400	6103	TW0865	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
401	6103	TW0866	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
402	6103	TW0867	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
403	6103	TW0868	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
404	6103	TW0869	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
405	6103	TW0870	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
406	6103	TW0871	-	Tuen Hi Road near Tuen Wui Street	Fell	-	-	-	-	-	-	Missing
407	6103	TW0872	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
408	6103	TW0873	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
409	6103	TW0874	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
410	6103	TW0875	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
411	6103	TW0876	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
412	6103	TW0877	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
413	6103	TW0878	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
414	6103	TW0879	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
415	6103	TW0880	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
416	6102	TW0881	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	07-Oct-10	17-Dec-10	17-Mar-11	Transplanted
417	6102	TW0882	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	06-Sep-10	07-Oct-10	12-Mar-11	Transplanted
418	6102	TW0883	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	04-Sep-10	07-Oct-10	12-Mar-11	Transplanted
419	6102	TW0884	苦楝	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	28-Sep-10	23-Mar-11	24-Mar-11	31/8 First Time
420	6102	TW0885	苦楝	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	28-Sep-10	23-Mar-11	24-Mar-11	31/8 First Time
421	6102	TW0886	秋楓樹	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	07-Oct-10	28-Mar-11	29-Mar-11	31/8 First Time
422	6102	TW0887	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
423	6102	TW0888	白千層	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	25-Sep-10	25-Sep-10	09-Nov-10	17-Jan-11	Transplanted
424	6102	TW0889	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
425	6101	TW0890	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
426	6101	TW0891	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	06-Oct-10	09-Nov-10	Transplanted
427	6101	TW0892	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	01-Sep-10	06-Oct-10	08-Nov-10	Transplanted
428	6101	TW0893	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	31-Aug-10	06-Oct-10	08-Nov-10	Transplanted
429	6101	TW0894	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	31-Aug-10	06-Oct-10	08-Nov-10	Transplanted
430	6101	TW0895	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	02-Sep-10	20-Nov-10	20-Nov-10	Transplanted
431	6101	TW0896	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	04-Sep-10	06-Oct-10	04-Nov-10	Transplanted
432	6101	TW0897	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	05-Oct-10	04-Nov-10	Transplanted
433	6101	TW0898	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	04-Sep-10	05-Oct-10	04-Nov-10	Transplanted
434	6101	TW0899	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	05-Oct-10	08-Nov-10	Transplanted
435	6101	TW0900	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	04-Sep-10	05-Oct-10	06-Dec-10	Transplanted
436	6101	TW0901	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	08-Nov-10	Transplanted
437	6101	TW0902	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	09-Oct-10	09-Apr-11	09-Apr-11	Undergr'd UU
438	6101	TW0903	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	04-Oct-10	07-Dec-10	Transplanted
439	6101	TW0904	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	04-Oct-10	09-Nov-10	Transplanted
440	6101	TW0905	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	04-Sep-10	05-Oct-10	20-Nov-10	Transplanted
441	6101	TW0906	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	04-Oct-10	06-Dec-10	Transplanted
442	6101	TW0907	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	04-Oct-10	07-Dec-10	Transplanted

443	6101	TW0908	洋紫荆	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	07-Oct-10	11-Dec-10	Transplanted
444	6101	TW0909	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	09-Dec-10	09-Dec-10	Transplanted
445	6101	TW0910	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	09-Dec-10	09-Dec-10	Transplanted
446	6101	TW0911	烏柏	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	03-Sep-10	08-Dec-10	08-Dec-10	Transplanted
447	6101	TW0912	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	10-Dec-10	10-Dec-10	10-Dec-10	Transplanted
448	6101	TW0913	烏柏	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	13-Dec-10	13-Dec-10	Transplanted
449	6101	TW0914	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	03-Sep-10	06-Oct-10	15-Dec-10	Transplanted
450	6101	TW0915	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	02-Sep-10	06-Oct-10	15-Dec-10	Transplanted
451	6101	TW0916	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	15-Dec-10	30-Aug-10	02-Sep-10	06-Oct-10	-	Poor Health
452	6101	TW0917	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	02-Sep-10	15-Dec-10	18-Jan-11	Transplanted
453	6101	TW0918	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
454	6101	TW0919	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	02-Sep-10	04-Oct-10	15-Dec-10	Transplanted
455	6101	TW0920	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	by other
456	6101	TW0921	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
457	6101	TW0922	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	15-Dec-10	Transplanted
458	6101	TW0923	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
459	6101	TW0924	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
460	6101	TW0925	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
461	6101	TW0926	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
462	6101	TW0927	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
463	6101	TW0928	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
464	6101	TW0929	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
465	6101	TW0930	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
466	6101	TW0931	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
467	6101	TW0932	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	04-Jan-11	Night Work
468	6101	TW0933	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	04-Jan-11	Night Work
469	6101	TW0934	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	04-Jan-11	Night Work
470	6101	TW0935	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
471	6101	TW0936	石栗	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
472	6101	TW0937	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
473	6101	TW0938	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	05-Jan-11	Night Work
474	6101	TW0939	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	05-Jan-11	Night Work
475	6101	TW0940	石栗	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
476	6101	TW0941	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
477	6101	TW0942	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
478	6101	TW0943	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	04-Jan-11	Night Work
479	6101	TW0944	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
480	6101	TW0945	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	05-Jan-11	Night Work
481	6101	TW0946	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
482	6101	TW0947	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	05-Jan-11	Night Work
483	6101	TW0948	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work
484	6101	TW0949	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work
485	6101	TW0950	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
486	6101	TW0951	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work
487	6101	TW0952	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
488	6101	TW0953	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
489	6101	TW0954	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
490	6101	TW0955	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
491	6101	TW0956	-	Tuen Mun Road A Bound near Yan Ching Street	Remove	-	-	-	-	-	-	Missing
492	6101	TW0957	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
493	6101	TW0959	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	

494	6101	TW0960	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
495	6101	TW0961	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
496	6101	TW0962	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
497	6101	TW0963	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
498	6101	TW0966	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
499	6101	TW0969	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
500	6101	TW0973	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	18-May-11	Transplanted
501	6101	TW0974	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	18-May-11	Transplanted
502	6101	TW0975	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	17-Dec-10	17-May-11	Transplanted
503	6101	TW0976	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	17-Dec-10	17-May-11	Transplanted
504	6101	TW0977	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	17-May-11	Transplanted
505	6101	TW0978	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	17-May-11	Transplanted
506	6101	TW0979	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
507	6101	TW0980	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
508	6101	TW0981		Yan Oi Tong Circuit Planter Area	Remove	-	-	-	-	-	-	Missing
509	6101	TW0982	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
510	6101	TW0983	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	24-Nov-10	24-Nov-10	24-Nov-10	Transplanted
511	6101	TW0984	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
512	6101	TW0985	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
513	6101	TW0986	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
514	6101	TW0987	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
515	6101	TW0988	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	09-Sep-10	15-Oct-10	Transplanted
516	6101	TW0989	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	09-Sep-10	27-Oct-10	Transplanted
517	6101	TW0990	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
518	6101	TW0991	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	14-Oct-10	-	-	-	-	
519	6101	TW0992	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
520	6101	TW0993	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
521	6101	TW0994	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	14-Oct-10	14-Oct-10	Transplanted
522	6101	TW0995	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	24-Nov-10	24-Nov-10	24-Nov-10	Transplanted
523	6101	TW0996	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	14-Oct-10	14-Oct-10	Transplanted
524	6101	TW0997	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
525	6101	TW0998	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
526	6101	TW0999	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
527	6101	TW1000	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
528	6101	TW1001	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
529	6101	TW1002	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
530	6101	TW1003	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
531	6101	TW1004	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
532	6101	TW1005	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	06-Aug-10	08-Sep-10	13-Oct-10	Transplanted
533	6101	TW1006	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted
534	6101	TW1007	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	30-Aug-10	12-Oct-10	12-Oct-10	Transplanted
535	6101	TW1008	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	13-Oct-10	13-Oct-10	Transplanted
536	6101	TW1009	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted
537	6101	TW1010	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
538	6101	TW1011	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	13-Oct-10	13-Oct-10	13-Oct-10	Transplanted
539	6101	TW1012	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
540	6101	TW1013	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	09-Aug-10	12-Oct-10	12-Oct-10	Transplanted
541	6101	TW1014	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	20-Aug-10	12-Oct-10	12-Oct-10	Transplanted
542	6101	TW1015	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted
543	6101	TW1016	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	06-Aug-10	08-Sep-10	27-Oct-10	Transplanted
544	6101	TW1017	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	08-Oct-10	Transplanted

545	6101	TW1018	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	30-Aug-10	05-Oct-10	08-Oct-10	Transplanted
546	6101	TW1019	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	03-Aug-10	-	-	-	-	
547	6101	TW1020	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	02-Aug-10	-	-	-	-	
548	6101	TW1021	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	07-Aug-10	08-Sep-10	08-Oct-10	Transplanted
549	6101	TW1022	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	25-Nov-10	25-Nov-10	25-Nov-10	Transplanted
550	6101	TW1023	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	07-Aug-10	10-Sep-10	08-Oct-10	Transplanted
551	6101	TW1024	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	08-Oct-10	Transplanted
552	6101	TW1025	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	09-May-11	Not Yet	
553	6101	TW1026	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	10-May-11	Not Yet	
554	6101	TW1027	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	03-Aug-10	-	-	-	-	
555	6101	TW1028	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	25-Nov-10	25-Nov-10	25-Nov-10	Transplanted
556	6101	TW1029	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	26-Nov-10	26-Nov-10	26-Nov-10	Transplanted
557	6101	TW1030	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	09-May-11	Not Yet	
558	6101	TW1031	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	09-May-11	Not Yet	
559	6101	TW1032	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	10-May-11	Not Yet	
560	6101	TW1033	大葉合歡	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
561	6101	TW1034	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	10-May-11	Not Yet	
562	6101	TW1035	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	10-May-11	Not Yet	
563	6101	TW1036	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	18-Oct-10	Transplanted
564	6101	TW1037	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	13-Nov-10	Transplanted
565	6101	TW1038	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	09-Aug-10	09-Sep-10	19-Oct-10	Transplanted
566	6101	TW1039	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
567	6101	TW1040	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
568	6101	TW1041	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
569	6101	TW1042	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
570	6101	TW1043	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
571	6101	TW1044	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	10-May-11	Not Yet	
572	6101	TW1045	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	07-Aug-10	09-Sep-10	28-Oct-10	Transplanted
573	6101	TW1046	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	09-Sep-10	13-Nov-10	13-Nov-10	Transplanted
574	6101	TW1047	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	26-Nov-10	26-Nov-10	26-Nov-10	Transplanted
575	6101	TW1048	鳳凰木	Yan Oi Tong Circuit Planter Area	Fell	Retain	30-Mar-11	-	-	-	-	
576	6101	TW1049	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Sep-10	09-Sep-10	19-Oct-10	19-Oct-10	Transplanted
577	6101	TW1050	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	19-Oct-10	Transplanted
578	6101	TW1051	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	02-Apr-11	10-May-11	Not Yet	
579	6101	TW1052	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	19-Oct-10	Transplanted
580	6101	TW1053	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	
581	6101	TW1054	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	10-May-11	Not Yet	
582	6101	TW1055	藍花楹	Yan Oi Tong Circuit Planter Area	Fell	Retain	30-Mar-11	-	-	-	-	
583	6101	TW1056	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	
584	6101	TW1057	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	
585	6101	TW1058	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	04-Aug-10	-	-	-	-	
586	6101	TW1059	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	04-Aug-10	-	-	-	-	
587	6101	TW1060	大葉合歡	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
588	6101	TW1061	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
589	6101	TW1062	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
590	6101	TW1063	-	Yan Oi Tong Circuit Planter Area	Remove	-	-	-	-	-	-	
591	6101	TW1065	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
592	6101	TW1066	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
593	6101	TW1067	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
594	6101	TW1068	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
595	6101	TW1069	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work

596	6101	TW1070	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
597	6101	TW1071	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
598	6101	TW1072	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
599	6101	TW1073	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
600	6101	TW1074	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
601	6101	TW1075	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
602	6101	TW1076	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
603	6101	TW1077	雙翼豆	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
604	6101	TW1078	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
605	6101	TW1079	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
606	6101	TW1080	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
607	6101	TW1081	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
608	6101	TW1082	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
609	6101	TW1083	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
610	6101	TW1084	洋紫荊	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
611	6101	TW1085	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
612	6101	TW1086	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
613	6101	TW1087	洋紫荊	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
614	6101	TW1088	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	
615	6101	TW1089	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
616	6101	TW1090	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
617	6101	TW1091	銀合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
618	6101	TW1092	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
619	6101	TW1093	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
620	6101	TW1094	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
621	6101	TW1095	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
622	6101	TW1096	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Missing	-	-	-	-	-	Missing
623	6101	TW1097	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
624	6101	TW1098	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
625	6101	TW1099	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
626	6109	TW1100	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
627	6109	TW1101	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
628	6109	TW1102	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
629	6109	TW1103	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
630	6109	TW1104	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
631	6109	TW1105	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
632	6109	TW1106	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
633	6109	TW1107	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
634	6109	TW1108	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
635	6105	TW1143	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
636	6105	TW1144	-	Tsing Sin Playground	Transplant	Missing	-	-	-	-	-	
637	6105	TW1145	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
638	6105	TW1146	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
639	6105	TW1147	-	Tsing Sin Playground	Transplant	Missing	-	-	-	-	-	
640	6105	TW1148	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	20-Sep-10	25-Oct-10	Transplanted
641	6105	TW1149	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	20-Sep-10	25-Oct-10	Transplanted
642	6105	TW1150	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
643	6105	TW1151	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
644	6105	TW1152	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
645	6105	TW1153	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
646	6105	TW1154	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-

647	6105	TW1155	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
648	6105	TW1156	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
649	6105	TW1157	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
650	6105	TW1158	馬拉巴栗	Tsing Hoi Circuit near RCP	Transplant	Transplant	N/A	31-Aug-10	02-Sep-10	04-Oct-10	25-Oct-10	Transplanted
651	6105	TW1161	血桐	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
652	6105	TW1162	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
653	6105	TW1163	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
654	6105	TW1164	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
655	6105	TW1165	銀合歡	Tsing Hoi Circuit near RCP	Remove	Remove	21-Aug-10	-	-	-	-	
656	6108	TW1166	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
657	6108	TW1167	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
658	6108	TW1168	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
659	6108	TW1169	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
660	6108	TW1170	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
661	6108	TW1171	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
662	6108	TW1172	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
663	6108	TW1173	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
664	6108	TW1174	木麻黃	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
665	6108	TW1182	木麻黃	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
666	6108	TW1183	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
667	6108	TW1185	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
668	6108	TW1186	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
669	6108	TW1187	木麻黃	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
670	6108	TW1190	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
671	6108	TW1191	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
672	6108	TW1192	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
673	6108	TW1193	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
674	6108	TW1194	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
675	6108	TW1195	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
676	6108	TW1196	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
677	6104	TW1200	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
678	6104	TW1201	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
679	6104	TW1202	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
680	6104	TW1203	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
681	6104	TW1204	-	Tsing Hoi Circuit near Tsing Wu Square	Fell	-	-	-	-	-	-	Missing
682	6104	TW1205	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
683	6104	TW1206	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
684	6104	TW1207	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
685	6104	TW1208	楓香	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
686	6104	TW1209	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
687	6104	TW1210	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
688	6104	TW1211	鳳凰木	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
689	6104	TW1212	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
690	6104	TW1213	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
691	6104	TW1214	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
692	6104	TW1215	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
693	6104	TW1216	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
694	6104	TW1217	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
695	6104	TW1218	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
696	6104	TW1219	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
697	6104	TW1220	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work

698	6104	TW1221	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
699	6104	TW1222	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
700	6104	TW1223	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
701	6104	TW1224	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
702	6104	TW1225	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
703	6104	TW1226	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
704	6104	TW1227	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
705	6104	TW1228	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
706	6104	TW1229	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
707	6104	TW1230	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
708	6104	TW1231	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
709	6104	TW1232	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
710	6104	TW1233	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
711	6104	TW1234	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	21-Oct-10	-	-	-	-	
712	6104	TW1235	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
713	6104	TW1236	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
714	6104	TW1237	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Feb-11	22-Feb-11	Night Work
715	6104	TW1238	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	10-Aug-10	-	-	-	-	
716	6104	TW1239	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Feb-11	26-Feb-11	Transplanted
717	6104	TW1240	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Feb-11	24-Feb-11	Transplanted
718	6104	TW1241	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Jan-11	08-Mar-11	Transplanted
719	6104	TW1242	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Jan-11	08-Mar-11	Transplanted
720	6104	TW1243	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Jan-11	09-Mar-11	Transplanted
721	6104	TW1244	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
722	6103	TW1245	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
723	6103	TW1248	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
724	6103	TW1249	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
725	6103	TW1250	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
726	6103	TW1251	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
727	6103	TW1257	宮粉羊蹄甲	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
728	6103	TW1258	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	-	-	-	-	-	-	Missing
729	6103	TW1259	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
730	6103	TW1260	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
731	6103	TW1261	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
732	6103	TW1262	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
733	6103	TW1263	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
734	6103	TW1264	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
735	6103	TW1265	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
736	6103	TW1266	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
737	6103	TW1267	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
738	6103	TW1268	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	24-Nov-10	-	-	-	-	Night Work
739	6103	TW1269	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
740	6103	TW1270	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
741	6103	TW1271	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
742	6103	TW1272	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
743	6103	TW1273	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
744	6103	TW1274	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
745	6103	TW1275	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
746	6103	TW1276	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
747	6103	TW1277	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
748	6103	TW1278	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	

749	6103	TW1279	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
750	6103	TW1280	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
751	6103	TW1281	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
752	6103	TW1282	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
753	6103	TW1283	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
754	6103	TW1284	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
755	6103	TW1285	朴樹	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
756	6103	TW1286	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Remove	-	23-Aug-10	-	-	-	-	
757	6103	TW1287	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
758	6103	TW1288	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
759	6103	TW1289	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
760	6103	TW1290	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
761	6103	TW1291	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
762	6103	TW1292	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
763	6103	TW1293	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
764	6103	TW1294	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
765	6103	TW1295	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
766	6103	TW1296	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
767	6103	TW1297	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
768	6103	TW1298	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
769	6103	TW1299	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
770	6103	TW1300	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
771	6103	TW1301	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
772	6103	TW1302	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
773	6104	TW1303	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	30-Sep-10	30-Sep-10	Transplanted
774	6104	TW1304	洋紫荊	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	11-Sep-10	30-Sep-10	30-Sep-10	Transplanted
775	6104	TW1305	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	30-Sep-10	30-Sep-10	Transplanted
776	6104	TW1306	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	25-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
777	6104	TW1307	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	25-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
778	6104	TW1308	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
779	6107	TW1309	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
780	6107	TW1310	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	23-Dec-10	Not Yet	Not Yet	
781	6107	TW1311	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
782	6107	TW1312	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
783	6107	TW1313	朴樹	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	
784	6107	TW1315	朴樹	Castle Peak Road J/O Tuen Hing Road	Transplant	Retain	-	-	-	-	-	
785	6107	TW1316	檸檬桉	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	
786	6107	TW1340	鳳凰木	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	Tree Pruning on 30/5
787	6107	TW1341	鳳凰木	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	Tree Pruning on 30/5
788	6103	TW1369	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	05-Jan-11	26-Feb-11	Night Work
789	6103	TW1370	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	05-Jan-11	26-Feb-11	Night Work
790	6103	TW1371	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	27-Aug-10	-	-	-	-	
791	6103	TW1372	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	01-Dec-10	-	-	-	-	
792	6103	TW1373	宮粉羊蹄甲	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	05-Jan-11	26-Feb-11	Night Work
793	6103	TW1374	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	27-Aug-10	-	-	-	-	
794	6103	TW1381	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	31-Dec-10	01-Mar-11	Night Work
795	6103	TW1382	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	31-Dec-10	01-Mar-11	Night Work
796	6103	TW1383	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	03-Mar-11	Night Work
797	6103	TW1384	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	02-Mar-11	Night Work
798	6103	TW1385	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	02-Mar-11	Night Work
799	6103	TW1386	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	31-Dec-10	03-Mar-11	Night Work

800	6103	TW1387	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	29-Dec-10	04-Mar-11	Night Work
801	6102	TW1414	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	23-Dec-10	01-May-11	Night Work
802	6102	TW1415	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	12-Feb-11	21-May-11	17-Dec-10
803	6102	TW1416	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	16-Dec-10	01-May-11	Night Work
804	6102	TW1417	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	17-Dec-10	01-May-11	Night Work
805	6102	TW1418	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	16-Dec-10	01-May-11	Night Work
806	6102	TW1419	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	23-Dec-10	19-May-11	
807	6102	TW1420	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	13-Feb-11	15-Feb-11	09-Apr-11	20-May-11	Big tree crown
808	6102	TW1421	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
809	6102	TW1422	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	28-Sep-10	04-Dec-10	04-Dec-10	Transplanted
810	6102	TW1423	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	18-Sep-10	-	-	-	-	
811	6101	TW1425	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	17-Dec-10	19-Jan-11	21-May-11	
812	6101	TW1426	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	17-Dec-10	19-Jan-11	14-Feb-11	27/9 First Root
813	6101	TW1427	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	17-Dec-10	19-Jan-11	14-Feb-11	Transplanted
814	6101	TW1428	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	16-Dec-10	19-Jan-11	12-Feb-11	Transplanted
815	6101	TW1429	藍花楸	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	04-Dec-10	04-Dec-10	Transplanted
816	6101	TW1430	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	03-Dec-10	03-Dec-10	Transplanted
817	6101	TW1431	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	03-Dec-10	03-Dec-10	Transplanted
818	6101	TW1432	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
819	6101	TW1433	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
820	6101	TW1434	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	28-Sep-10	17-Dec-10	11-Feb-11	Transplanted
821	6101	TW1435	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
822	6101	TW1436	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
823	6101	TW1437	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
824	6101	TW1438	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
825	6101	TW1439	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Remove	-	-	-	-	-	-	
826	6101	TW1440	血桐	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	23-Dec-10	14-Feb-11	Transplanted
827	6101	TW1441	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	16-Dec-10	18-Jan-11	Transplanted
828	6101	TW1442	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	16-Dec-10	20-Jan-11	12-Feb-11	Transplanted
829	6101	TW1443	蒲葵	Tuen Mun Road B Bound Slip Road to Pui To Road	Retain	Retain	-	-	-	-	-	
830	6101	TW1444	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Retain	Retain	-	-	-	-	-	
831	6101	TW1445	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	19-Feb-11	Transplanted
832	6101	TW1446	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	19-Feb-11	Transplanted
833	6101	TW1447	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	24-Sep-10	16-Dec-10	19-Feb-11	Transplanted
834	6101	TW1448	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	19-Feb-11	17-Sep-10	25-Sep-10	16-Dec-10	-	Poor Health
835	6101	TW1449	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
836	6101	TW1450	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	21-Feb-11	Transplanted
837	6101	TW1451	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
838	6101	TW1452	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	21-Feb-11	Transplanted
839	6101	TW1453	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	06-Oct-10	-	-	-	-	Poor Health
840	6101	TW1456	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Remove	-	-	-	-	-	-	
841	6101	TW1457	大葉桉	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
842	6101	TW1458	大葉桉	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
843	6101	TW1459	-	Yan Oi Tong Circuit Car Park	Fell	-	16-Nov-10	-	-	-	-	
844	6101	TW1460	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
845	6101	TW1461	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
846	6101	TW1462	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	-	-	-	-	-	by other
847	6101	TW1466	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
848	6101	TW1467	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
849	6101	TW1468	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
850	6101	TW1469	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	

851	6101	TW1470	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
852	6101	TW1471	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
853	6101	TW1472	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
854	6101	TW1473	白千層	Centre Median near San Tsing Street	Retain	Retain	-	-	-	-	-	
855	6101	TW1474	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
856	6101	TW1475	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
857	6101	TW1476	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
858	6101	TW1477	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
859	6101	TW1478	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
860	6101	TW1479	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
861	6101	TW1480	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
862	6101	TW1481	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
863	6101	TW1482	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
864	6108	TW1526	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
865	6108	TW1527	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
866	6108	TW1528	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
867	6108	TW1529	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
868	6108	TW1530	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
869	6108	TW1531	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
870	6108	TW1532	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
871	6108	TW1533	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
872	6108	TW1534	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
873	6108	TW1535	石栗	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
874	6108	TW1536	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
875	6108	TW1537	木棉	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
876	6108	TW1538	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
877	6108	TW1539	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
878	6108	TW1540	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
879	6108	TW1541	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	12-May-11	Not Yet	
880	6108	TW1542	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	12-May-11	Not Yet	
881	6108	TW1543	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	12-May-11	Not Yet	
882	6108	TW1544	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	12-May-11	Not Yet	
883	6108	TW1545	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	12-May-11	Not Yet	
884	6108	TW1546	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	12-May-11	Not Yet	
885	6108	TW1547	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	12-May-11	Not Yet	
886	6108	TW1548	白千層	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
887	6108	TW1549	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
888	6108	TW1550	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
889	6108	TW1551	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
890	6108	TW1552	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
891	6105	TW1553	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	21-Sep-10	21-Sep-10	Transplanted
892	6105	TW1554	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	21-Sep-10	21-Sep-10	Transplanted
893	6105	TW1555	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	21-Sep-10	21-Sep-10	Transplanted
894	6105	TW1556	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
895	6105	TW1557	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
896	6105	TW1558	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
897	6105	TW1559	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
898	6105	TW1560	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
899	6105	TW1561	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
900	6105	TW1562	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
901	6105	TW1563	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted

[illegible]

[illegible]

1004	6108	TWA7	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	-	Not Yet	-	-	-	-	
1005	6108	TWA8	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1006	6108	TWA9	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1007	6108	TWA10	石栗	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1008	6108	TWA11	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1009	6108	TWA12	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1010	6109	TWA30	火焰木	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	07-May-11	07-May-11	Not Yet	Not Yet	
1011	6109	TWA31	火焰木	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	07-May-11	07-May-11	Not Yet	Not Yet	
1012	6109	TWA32	木棉	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	09-May-11	16-May-11	Not Yet	Not Yet	
1013	6101	TWA33	鳳凰木	Yan Oi Tong Circuit Car Park	Fell	-	14-Mar-11	-	-	-	-	
1014	6101	TWA34	洋蹄甲	Yan Oi Tong Circuit Car Park	Fell	-	14-Mar-11	-	-	-	-	
1015	6101	TWA35	蒲葵	Yan Oi Tong Circuit Car Park	Transplant	-	N/A	14-Mar-11	15-Apr-11	18-May-11	18-May-11	Transplanted
1016	6101	TWA36	蒲葵	Yan Oi Tong Circuit Car Park	Transplant	-	N/A	14-Mar-11	15-Apr-11	18-May-11	18-May-11	Transplanted
1017	6104	TWA37	洋蹄甲	Tsing Wui Street Car Park	Fell	-	14-Mar-11	-	-	-	-	
1018	6104	TWA38	火焰木	Tsing Wui Street Car Park	Transplant	-	N/A	14-Mar-11	31-Mar-11	13-May-11	13-May-11	Transplanted
1019	6103	TWA39	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work
1020	6103	TWA40	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work
1021	6103	TWA41	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work

24 nos. of New trees under UPTRA No.1 & Revised the proposed treatment

26 nos. of big crown trees

29 nos. of trees in poor health (Application No.2)

Appendix J

**Monthly Summary
Waste Flow Table**



Monthly Summary of Waste Flow Table for 2011 (year)

Name of Person completing the Record: Marko Chan

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(see Note 1) (in '000m ³)						(see Note 2) (in '000 Kg)		
Jan	0.536250	Nil	Nil	Nil	0.536250	0.00300	0.35000	Nil	Nil	0.053630
Feb	1.823250	Nil	0.053625	Nil	1.769625	0.10211	Nil	Nil	Nil	0.039000
Mar	2.676375	Nil	Nil	Nil	2.676375	2.40500	0.41700	Nil	Nil	0.102375
Apr	3.144375	Nil	Nil	0.136500	3.007875	2.72000	Nil	Nil	Nil	0.087750
May	2.968875	Nil	Nil	Nil	2.968875	Nil	0.37100	Nil	Nil	0.053625
Jun										
Sub-total	11.149125	Nil	0.053625	0.136500	10.959000	5.23011	1.13800	Nil	Nil	0.336380
Jul										
Aug										
Sept										
Oct										
Nov										
Dec										
Total										

Notes:

- (1) Broken concrete for recycling into aggregates.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (3) Use the conversion factor: 1 full load of dumping truck being equivalent to 6.5m³ by volume.

Appendix K

**Environmental
Monitoring Programme
for Coming Month**

Agreement No. CE 22/2005 (HY) Traffic Improvement to Tuen Mun Road Town Centre Section
Tentative Impact Monitoring Schedule - June 2011 Revision 1

Date		Air Quality	Noise	Landscape & Visual	Site Inspection
		24-hours TSP	L _{Aeq} , 30 min		
1-Jun-11	Wed				
2-Jun-11	Thu				
3-Jun-11	Fri				
4-Jun-11	Sat				
5-Jun-11	Sun				
6-Jun-11	Mon				
7-Jun-11	Tue				
8-Jun-11	Wed				
9-Jun-11	Thu				SSEMC
10-Jun-11	Fri				
11-Jun-11	Sat				
12-Jun-11	Sun				
13-Jun-11	Mon				
14-Jun-11	Tue				
15-Jun-11	Wed				
16-Jun-11	Thu				
17-Jun-11	Fri				
18-Jun-11	Sat				
19-Jun-11	Sun				
20-Jun-11	Mon				
21-Jun-11	Tue				
22-Jun-11	Wed				
23-Jun-11	Thu				
24-Jun-11	Fri				
25-Jun-11	Sat				
26-Jun-11	Sun				
27-Jun-11	Mon				
28-Jun-11	Tue				
29-Jun-11	Wed				
30-Jun-11	Thu				

	Public Holiday
	Monitoring Day

Monitoring Details

Monitoring	Quantity	Locations	Parameters
Air Quality	6	Mrs.Aw Boon Haw Secondary School Tai Tung Pui Social Service Building Wu Siu Kui Primary School Choi Cheung Kok Secondary School Tuen Mun Town Hall Yan Oi Tong Community and Sport Centre	24-hour TSP, Wind speed / direction
Noise	6	Kam Fai Garden Tai Tung Pui Social Service Building Yuen Yuen Primary School Wu Siu Kui Primary School Tuen King Building Choi Cheung Kok Secondary School	L _{Aeq} (30 min), L ₁₀ , L ₉₀

Appendix L

Complaint Log

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Complaint Log

ET's Complaint Log Ref. no.	Incoming Complaint Ref no.	Name of Complainant	Date of Complaint receive	Complaint Date/ Period	Complaint Location	Area of Concern	Details of Complaint	Date of Complaint received by ET	ET's Investigation Date	Investigation / Mitigation Measures	Validity to the Project	Status
C005-TCS	A complaint was received by ICC on 23 May 11 and the Supervising Officer Representative was informed via the e-mail on same date.	Unknown	23 May 11	Daytime (around 15:20) of 23 May 11	The section of TMR (to Yuen Long direction) between Pui To Road and Yan Oi Tong	Water	The complaint was related to the cleaning water spillage to TMR during the complaint period	24 May 11	25 May ~ 9 Jun 11	<p>As confirmed by the Contractor and Supervising Officer's Representative, the floor cleaning activities was carried out at the site entrance of Pui To Road during the complaint period. The cleaning water was spilled to TMR and affected the travelling vehicles. Therefore, it is concluded that the complaint was work-related under the Project.</p> <p>As advised by the Contractor and Supervising Officer's Representative, the workers were reminded to pay attention during cleaning activities to avoid water spillage to TMR after the complaint was received. Based on the weekly site inspections on 26 May and 2 June 11, the site condition was satisfactory and no water spillage was observed.</p> <p>Nevertheless, ET recommended that the Contractor should undertake following mitigation measures to minimize the nuisance.</p> <ol style="list-style-type: none">1. Improve the working practices to minimize the nuisance during the cleaning activities as far as possible; and2. Enhance the workers awareness by regular training to minimize nuisance during the cleaning activities.	Yes	Closed on 10 Jun 11
