

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk


Materialab

Ref No.: 100440EN120861

Contract No. EP/SP/58/08
Sludge Treatment Facilities
Environmental Monitoring and Audit Report
For
August 2012

Materialab Ref No.: 100440EN120861

Certified by :



John K. M. Ho
(Environmental Team Leader)

Date :

04 September 2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

CONTENTS

1. Executive Summary
2. Introduction
3. General Review
4. Construction Phase Environmental Monitoring
5. Construction Site Environmental Audit
6. Summary of Complaints, Summons and Successful Prosecutions
7. Works Programme for September 2012
8. Monitoring Schedule for September 2012
9. Comments and Conclusions for the Reporting Period

Appendices:

- Appendix 1: Water Quality Monitoring Location
- Appendix 2: Equipment Calibration Certificates
- Appendix 3: Stream and Marine Water Quality Monitoring Data
- Appendix 4: Graphical Presentation of Monitoring Data
- Appendix 5: Construction Program
- Appendix 6: Management Structure and Organization Chart
- Appendix 7: Event / Action Plan for Water Quality
- Appendix 8: Implementation Schedule of Mitigation Measures
- Appendix 9: Incident Report on Action Level or Limit Level Non-compliance

List of Tables:

- Table 3.1 The Contact Persons and Telephone Numbers of Key Personnel
- Table 3.2 Summary of Monitored Parameters
- Table 3.3 Action and Limit Levels for Marine and Stream Water Quality
- Table 3.4 Action Level for Landfill Gas Measurement
- Table 4.1 Method Statements of Laboratory Analysis of Marine Water Quality
- Table 4.2 Method Statements of Laboratory Analysis of Stream Water Quality
- Table 4.3 Water Quality Monitoring Equipment
- Table 4.4. Monitoring Schedule from 25 July to 24 August 2012
- Table 4.5 Water Quality Monitoring Results
- Table 4.6 Summary of Exceedances from 25 July to 24 August 2012
- Table 4.7 Landfill Gas Monitoring Equipment
- Table 4.8 Summary of Landfill Gas Monitoring

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.9	Ecological Survey Checklist for August 2012
Table 4.10	Record of Implementation of the Proposed Landscape and Visual Mitigation Measures in Construction Phase
Table 4.11	Photographic Record of Landscape and Visual Impact Survey
Table 5.1	Waste Flow Summary
Table 6.1	Summary of Environmental Complaints and Prosecutions
Table 8.1	Monitoring Schedule for September 2012

List of Figures:

Figure 1.1	Construction Works Area
Figure 3.1	Site Layout Plan
Figure 3.2	WENT Landfill Gas Control Zone
Figure 4.1	Ecological Transect Route

Ref No.: 100440EN120861

1. Executive Summary

Construction work commenced on 22 December 2010. It was of main concern to ascertain whether there was any undesirable effect of the construction activities on various environmental parameters over the site area and the surrounding environment. Impact environmental monitoring on water quality, ecology and landscape and visual impact were carried out to acquire data for assessing any impact associated with the construction activities. This report covers the period from 25 July to 24 August 2012 inclusive.

Marine Water Quality

Pursuant to EM&A manual, marine water quality monitoring is required during the foundation piling. Piling work was commenced on 21 February 2011 while marine water quality monitoring was conducted during the foundation piling. The foundation piling work was completed on 13 October 2011 and the pre-bore piling of the STF was completed on 22 February 2012 (the post monitoring for marine water has been completed on 20 March 2012). Although marine water quality monitoring resumed on 03 July 2012 due to the commencement of pre-bore operation for sheet piling, the pre-bore operation as planned was not carry out. Therefore the impact marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

As far as the water quality was concerned, 2 events of non-compliance of Action / Limit levels for aluminium content were recorded in the reporting period.

The recorded exceedances are not caused by the construction activities so there was no action taken with regards to the action plan.

Stream Water Quality

As far as the water quality was concerned, 15 events of non-compliance of Action / Limit level on various monitored parameters were recorded in the reporting period.

The recorded exceedances are not caused by the construction activities so there was no action taken with regards to the action plan.

In general, the stream water quality was not significantly deteriorated after the commencement of the major construction works on 21 February 2011.

Landfill Gas Monitoring

Excavation works has been carried out within the WENT landfill consultation zone for the following construction activities during the reporting period: (1) Portion 1 (next to Plant B, foundations works for east marshalling area); (2) Portion 3 (next to Canteen, cable ducting) and (3) Portion 3 (next to T758). Landfill gas monitoring was carried out by a competent person during the operation and no exceedance was found.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Ref No.: 100440EN120861

Ecology Monitoring

Two surveys were conducted on 08 and 21 August 2012 at the Middle Lagoon. Total of 132 nos. of birds of 14 species was recorded on 21 August 2012. None of the birds showed any apparent signs of disturbance arising from the STF construction activities. All measures were followed to minimize the disturbance of the wildlife. No disturbance was observed while construction work in progress.

Landscape and Visual Monitoring

Landscape and visual impact monitoring was conducted on 06 and 20 of August 2012. Details are presented in Section 4.4.

Works Undertaken During Reporting Period

The construction phase commenced on 22 December 2010, major site activities conducted in the reporting period includes:

- Waterproofing;
- Steel Works;
- Strut Erection;
- Substructure Works: including reinforcement, formwork, concreting;
- Structure Works: including reinforcement, formwork, concreting;
- Assembly of Boiler;
- Structural Steel Erection;
- Roof Installation;
- Mechanical Installation;
- Bridge Construction;
- Heavy Lifting;
- Façade Installation;
- Delivery of Heavy Machineries;
- E & M Installation;
- Curtain Wall Installation;
- Gondola Operation;
- Inter Decoration;
- Precast Installation;
- Road Works;
- Space Truss Installation; and
- Glass and Steel Installation

Works area is shown in Figure 1.1

Reporting Changes and Future Key Issues

It is anticipated that the existing operation should not create significant nuisance and disturbance on the environmental aspects of air quality, noise level and water quality. Foundation piling was started on 21 February 2011 and completed on 13 October 2011. Additional pre-bore operation was completed on 22 February 2012. Contractor should implement proposed measures to minimize potential impact to the noise, air quality, stream and marine water quality, ecology and landscape.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Generation of site runoff is anticipated during rain season, the drainage systems should be maintained regularly to ensure wastewater could be treated properly. Loose and exposed surfaces should be compacted or covered to minimize soil erosion. Remove the stagnant water after the rainfall or provide pesticide to avoid mosquito breeding.

Complaints, Summons and Successful Prosecutions

As far as complaints, summons and successful prosecutions on the construction work in respect of the environmental protection and pollution control was concerned, there was no documented correspondence received in the reporting period.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

2. Introduction

This monthly report reviews the progress of the environmental monitoring and audit work at the site for Contract No. EP/SP/58/08 from 25 July 2012 to 24 August 2012 (the reporting period) and forecasts the activities for September 2012. The monitoring results for water quality are presented in Appendix 3 and the corresponding graphical plots are shown in Appendix 4. Findings of Ecology and Landscape monitoring are presented in Section 4.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Ref No.: 100440EN120861

3. General Review

3.1 Background

The Contractor, VW-VES (HK) Limited, has been awarded a contract by the Environmental Protection Department of the Government of the Hong Kong Special Administrative Region for the Sludge Treatment Facilities. The location of the site is shown in Figure 3.1.

The program commenced in November 2010 and is anticipated to complete in 2013.

The construction schedule will be based on the major works associated with the project. The major works under this contract include:

Incineration Plant

- a) Sludge receiving, storage and feeding system
- b) Fluidized bed incinerators
- c) Waste heat recovery and power generation system
- d) Flue gas treatment system
- e) Ash storage and handling system
- f) Residue storage and handling system
- g) Fluidized bed sand storage and handling system
- h) Reagent reception and storage system
- i) Process control and monitoring system

Ancillary and supporting Facilities

- a) Weighbridge
- b) Site security
- c) Administration building
- d) Vehicle washing facilities
- e) Maintenance workshop and utility yard
- f) Drainage system
- g) Sewerage system
- h) Sewage treatment works
- i) Water supply system
- j) Deodorization system

Construction program for the captioned project is enclosed in Appendix 5.

Fugro Technical Services Ltd. – Materialab Division (Materialab) has been commissioned by the client as the Environmental Team which comprises the monitoring staff and the environmental auditor to undertake the environmental monitoring and audit work for this project. The project management structure and organization chart is shown in Appendix 6.

The contact person and telephone numbers of key personnel for the captioned project are shown in Table 3.1.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Ref No.: 100440EN120861

Table 3.1 The Contact Persons and Telephone Numbers of Key Personnel

Company / Department	Role in the Contract	Contact Person	Telephone Number
VW-VES (HK) Limited	Contractor	Mr. Vincent Deleu	2253 2600
Environmental Protection Department	Employer	Mr. Kenneth Chan	2872 1800
Environmental Protection Department, EIAO	EIAO Officer	Mr. Thomas To	2835 1103
JACOBS	Employer Representative	Mr. Leslie Swann	2880 9788
Fugro Technical Services Ltd. – MaterialLab Division	Environmental Team	Mr. John Ho	2450 8233
BMT Asia Pacific Ltd.	Independent Environmental Checker	Ms. Claudine Lee	2241 9847

3.2 Summary of Environmental Monitoring and Audit (EM&A) Requirements

The EM&A program requires the monitoring of water quality prior to the commencement of and during the construction. A baseline report was prepared in December 2010 for the contract based on monitoring data acquired before the commencement of construction works.

Impact monitoring of water quality is to be undertaken at the designated monitoring stations. The monitored parameters are summarized in Table 3.2.

Action and Limit (AL) levels are established based on the data from the baseline report. Should the monitoring results indicate any non-compliance of AL levels, actions according to the Event / Action Plan in Appendix 7 are to be followed and appropriate environmental mitigation measures as in Appendix 8 are to be implemented to rectify the situation. The implementation status of mitigation measures is also shown in Appendix 8.

Impact ecology and visual survey are to be conducted at the construction area on regular basis. Monitoring parameters are tabulated in Table 3.2.

The Contractors (VW-VES (HK) Limited) is responsible for waste control within the construction site, removal of the waste material produced from the site and to implement any mitigation measures to minimize waste or redress problems arising from the waste from the site. The waste material may include any sewage, waste water or effluent containing sand, cement, silt or any other suspended or dissolved material to flow from the site onto any adjoining land, storm sewer, sanitary water, or any waste matter or refuse to be deposited anywhere within the site or onto any adjoining land.

The Contractor shall also pay attention to the Waste Disposal Ordinance, the Dumping at Sea Ordinance, the Public Health and Municipal Services Ordinance and the Water Pollution Control Ordinance, and carry out the appropriate waste management work. The relevant licence / permit, such as the effluent discharge licence, the chemical waste producer registration, etc. shall be obtained. The

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Contractor shall refer to the relevant booklets issued by EPD when applying for the licence / permit.

The environmental mitigation measures and status for waste management are summarized in Appendix 8.

Table 3.2 Summary of Monitored Parameters

Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Marine water	<ul style="list-style-type: none"> ▪ Cadmium ▪ Chromium ▪ Aluminium 	2 monitoring stations and 1 control station	Three days per week for mid-ebb and mid-flood tides during foundation piling of the STF.	Sampling is taken at three water depths, namely, 1m below water Surface, mid-depth and 1m above sea bed, except where the water depth be less than 6m, in which case the mid-depth station may be omitted. Shall the water depth be less than 3m, only the mid-depth station will be monitored.
Stream water	<ul style="list-style-type: none"> ▪ pH ▪ Turbidity ▪ Suspended solids ▪ Dissolved oxygen 	3 monitoring stations and 2 control stations	Three days per week for mid-ebb and mid-flood tides during site formation and foundation piling of the STF and construction of the access road.	<ul style="list-style-type: none"> ▪ Two consecutive measurements of DO concentration, DO saturation, turbidity and pH are taken at mid-depth at each location. ▪ Water samples for SS measurement is collected at the same depth at each location.
Ecology	Site condition and bird monitoring	Whole Middle Lagoon and 20m from the boundary of the Lagoon	<ul style="list-style-type: none"> ▪ Monthly monitoring for avifauna. ▪ Habitat monitoring at least twice per month. ▪ Monthly vegetation monitoring. 	<ul style="list-style-type: none"> ▪ Avifauna and their behavior. ▪ All birds seen and heard should be identified and counted. ▪ Signs of breeding of birds. ▪ Coverage of water and PFA filling activities in Middle Lagoon.
Landscape and Visual Impact	All measures, including compensatory planting, undertaken by both the Contractor and the specialist Landscape Sub-Contractor	East Lagoon	Biweekly.	Ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.

Ref No.: 100440EN120861

Table 3.2 (Con't)

Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Landfill gas	<ul style="list-style-type: none"> ▪ Oxygen ▪ Methane ▪ Carbon dioxide 	Excavation, operation in chamber and confined space within the WENT Landfill Control Zone. (See Figure 3.2)	During the construction and operation.	<ul style="list-style-type: none"> ▪ Excavation between 300mm to 1m deep: <ul style="list-style-type: none"> - Directly after the excavation has been completed. - Periodically whilst the excavation remains open. ▪ Excavation deeper than 1m: <ul style="list-style-type: none"> - At ground surface before excavations commences. - Immediately before any worker enters the excavation. - At the beginning of each working day for the entire period the excavation remains open. - Periodically whilst the excavation remains open.

3.3 Action and Limit Levels

Water Quality Limit

Environmental auditing on the monitoring data is to be undertaken based on the Action and Limit (AL) levels for water quality to check against any non-compliances.

The AL levels for monitored parameters are formulated from the baseline monitoring data. The AL levels for marine and stream water quality are tabulated in Table 3.3.

Table 3.3 Action and Limit Levels for Marine and Stream Water Quality

Parameters	Action Level	Limit Level
DO in mg/L (mid-depth)	≤ 5.16	≤ 4
SS in mg/L (mid-depth)	≥ 41 AND 120% of control station's SS on the same day of measurement	≥ 85 AND 130% of control station's SS on the same day of measurement
Turbidity in NTU (mid-depth)	≥ 36.4 AND 120% of control station's turbidity on the same day of measurement	≥ 78.9 AND 130% of control station's turbidity on the same day of measurement
pH	pH ≤ 7.55 or pH ≥ 8.11	pH ≤ 6 or pH ≥ 9

Ref No.: 100440EN120861

Table 3.3 (Con't)

Parameters	Action Level	Limit Level
Cadmium in µg/L	≥ 0.5	≥ 0.5
Chromium in µg/L	≥ 1	≥ 1
Aluminium in µg/L	≥ 20	≥ 20

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Landfill Gas Limit

Depending on the results of the measurements, actions required will be vary and should be set down by the Safety Officer or other appropriately qualified person. The actions shown in Table 3.4 should be referred as the minimum requirements to be encompassed.

Table 3.4 Action Level for Landfill Gas Measurement

Parameter	Measurement	Action
Oxygen	<19 %	<ul style="list-style-type: none"> ▪ Ventilate to restore oxygen to >19 %
	<18 %	<ul style="list-style-type: none"> ▪ Stop works ▪ Evacuate personnel / prohibit entry ▪ Increase ventilation to restore oxygen to >19 %
Methane	>10 % LEL (i.e. >0.5 % by volume)	<ul style="list-style-type: none"> ▪ Prohibit hot works ▪ Ventilate to restore methane to <10 % LEL
	>20 % LEL (i.e. >1 % by volume)	<ul style="list-style-type: none"> ▪ Stop works ▪ Evacuate personnel / prohibit entry ▪ Increase ventilation to restore methane to <10 % LEL
Carbon dioxide	>0.5 %	<ul style="list-style-type: none"> ▪ Ventilate to restore carbon dioxide to <0.5 %
	>1.5 %	<ul style="list-style-type: none"> ▪ Stop works ▪ Evacuate personnel / prohibit entry ▪ Increase ventilation to restore carbon dioxide to <0.5 %

Ref No.: 100440EN120861

4. Construction Phase Environmental Monitoring

The construction phase was commenced on 22 December 2010. During the construction phase, impact water quality monitoring for marine and stream is required. The monitoring locations are shown in Appendix 1.

4.1 Water Quality Monitoring**4.1.1 Monitoring Methodology***Marine Water Quality*

During the course of foundation piling of the STF, the impact conditions of marine water quality are measured at two monitoring stations and one control station with coordinates as shown in Appendix 1. The Environmental Team Leader shall agree with the IEC and EPD on all the monitoring stations.

During the course of foundation piling, impact monitoring shall be undertaken three days per week, at mid-flood and mid-ebb tides, with sampling and measurement at the designated monitoring stations.

The foundation piling of the STF has been completed on 13 October 2011 and the additional pre-bore piling of the STF has been completed on 22 February 2012 (the post monitoring for marine water was completed on 20 March 2012). Although marine water quality monitoring resumed on 03 July 2012 due to the commencement of pre-bore operation for sheet piling, the pre-bore operation as planned was not carry out. Therefore the impact marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

Samples are to be taken at three water depths, namely 1m below water surface, mid-water and 1m above seabed at both mid-flood and mid-ebb tides, except where the water depth is less than 6m, the mid-depth station may be omitted. Should the water depth be less than 3m, only mid-depth will be monitored.

Water samples should be kept in chilled condition (~4°C) during delivery to laboratory and before commencement of the analysis. The parameters of laboratory analysis include Cadmium, Chromium and Aluminium. The method statements are shown in Table 4.1.

Table 4.1 Method Statements of Laboratory Analysis of Marine Water Quality

Parameters	Method	Detection limit, µg/L
Cadmium	USEPA method 6020A	0.5
Chromium		1
Aluminium		20

Stream Water Quality

Monitoring of pH, turbidity level (NTU), suspended solids level (mg/L), and dissolved oxygen (mg/L) are conducted at the designated locations including three monitoring stations and two control stations as shown in Appendix 1. The method statements are shown in Table 4.2.

Ref No.: 100440EN120861

Dissolved oxygen, turbidity and pH are measured *in-situ* while suspended solids content is determined in a HOKLAS accredited laboratory.

Impact monitoring is undertaken three days per week during mid-ebb and mid-flood tides.

Pursuant to Clause 5.7.1.1 of the EM&A Manual, impact water quality monitoring shall be carried out during site formation, piling and construction of the access road. As the above mentioned site construction has been completed on 17 August 2012, four weeks post monitoring is commenced by 20 August 2012 and ended on 14 September 2012 inclusively.

Table 4.2 Method Statements of Laboratory Analysis of Stream Water Quality

Parameters	Method	Detection limit, mg/L
Suspended solids	APHA, 18 th edition, 2540D	1

4.1.2 Monitoring Equipment

The equipment employed for the monitoring are presented in Table 4.3 and the calibration certificates are attached in Appendix 2.

Table 4.3 Water Quality Monitoring Equipment

Equipment	Model	Parameters Measured
<i>Fieldwork – Marine Water Quality Monitoring</i>		
Global positioning system (GPS)	Trimble Scout Master / Magellan Colotrak	Positioning
Echo sounder	Eagle Magna 3	Depth
Water sampler	Kahlsico 135WB153	Water sampling
<i>Fieldwork – Surface Water Quality Monitoring</i>		
pH meter	YSI Professional Plus Model: Proplus - 4	pH
Dissolved oxygen meter		Dissolved oxygen
Salinity meter		Temperature
Turbidity meter	HACH 2100P	Salinity
Water sampler	Kahlsico 135WB153 / Pitcher	Turbidity
<i>Laboratory Analysis</i>		
Analytical balance	Ohaus AP210S	Water sampling
Oven	WIB-Binder IP120	Suspended solids
Vacuum pump	GAST DOA-P104-BN	Suspended solids

4.1.3 Review of the Construction Phase Monitoring Programme

The schedule for the marine and stream water monitoring programme in the reporting period is shown in Table 4.4.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.4 Monitoring Schedule of Stream and Marine Water from 25 July to 24 August 2012

SUN	MON	TUE	WED	THU	FRI	SAT
22 July	23	24	25 W* M*	26	27 W M	28
29	30 W M	31	01 Aug W M	02	03 W M	04
05	06 W M	07	08 W M	09	10 W M	11
12	13 W M	14	15 W M	16	17 W M**	18
19	20 W# M	21	22 W#	23	24 W#	25
26	27	28	29	30	31	

Legend: W – Stream water quality monitoring at C1, C2, W1, W2 and W3. Three days per week.

M – Marine water quality monitoring at DM4, M1 and M2. Three days per week.

Note: Marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

Four weeks post monitoring for stream water commenced by 20 August 2012 and ended on 14 September 2012 inclusively.

* Due to “Amber Rain” warning signal hoisted in the morning (25 July 2012), the schedule water quality monitoring (mid-flood tide) was cancelled. Monitoring at the afternoon was performed as schedule.

** Marine water quality monitoring on 17 August 2012 was cancelled due to the enforcement of strong wind signal no. 3.

4.1.4 Impact Water Quality Monitoring Result

The impact water quality monitoring data, laboratory results and QC data are shown in Appendix 3. The statistical analysis of the data is shown in Table 4.5. Graphical plot of average measurement is enclosed in Appendix 4.

During the course of the monitoring work, waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, and glass and steel installation were observed within the project area.

Table 4.5 Water Quality Monitoring Results (25 July to 24 August 2012)

Location	Parameters	Maximum	Minimum	Mean
<i>Stream Water Quality Result</i>				
W1	Dissolved Oxygen (mg/L)	7.13	5.19	5.95
	Turbidity (NTU)	86.00	3.90	15.34
	pH	7.80	7.10	7.62
	Suspended Solids (mg/L)	56.00	2.00	14.00
W2	Dissolved Oxygen (mg/L)	8.85	5.21	6.51
	Turbidity (NTU)	105.00	6.52	17.79
	pH	7.99	7.01	7.59
	Suspended Solids (mg/L)	110.00	7.00	20.00

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.5 (Con't)

Location	Parameters	Maximum	Minimum	Mean
Stream Water Quality Result				
W3	Dissolved Oxygen (mg/L)	9.72	5.17	6.92
	Turbidity (NTU)	108.00	3.49	13.81
	pH	8.06	7.00	7.62
	Suspended Solids (mg/L)	90.00	4.00	15.00
Marine Water Quality Result				
M1	Cadmium (µg/L)	< 0.5	< 0.5	< 0.5
	Chromium (µg/L)	< 1	< 1	< 1
	Aluminium (µg/L)	25	< 20	23
M2	Cadmium (µg/L)	< 0.5	< 0.5	< 0.5
	Chromium (µg/L)	< 1	< 1	< 1
	Aluminium (µg/L)	< 20	< 20	< 20

4.1.5 Summary of Non-compliances of the Environmental Quality Performance Limits from 25 July 2012 to 24 August 2012

Marine Water Quality

2 events of non-compliance regarding aluminium was recorded on 25 July 2012 (from 25 July 2012 to 24 August 2012). Details are refers to Appendix 9.

Table 4.6a Summary of Exceedances (Marine Water Quality) from 25 July 2012 to 24 August 2012

Date & Time	Location	Parameters
25 July 2012, 16:15 to 16:51 (Mid-Ebb)	M1: Surface Level	Aluminium : 25 µg/L (Limit Level Exceedance) Control Point - DM4 : <20 µg/L
	M1: Bottom Level	Aluminium : 22 µg/L (Limit Level Exceedance) Control Point - DM4 : <20 µg/L

Stream Water Quality

15 events of non-compliance regarding pH were recorded on various days from 25 July 2012 to 24 August 2012. Details are refers to Appendix 9.

Table 4.6b Summary of Exceedances (Stream Water Quality) from 25 July 2012 to 24 August 2012

Date & Time	Location	Parameters
25 July 2012, 16:08 to 17:36 (Mid-Ebb)	W2	pH : 7.12 (Action Level Exceedance) C1 : 7.22 C2 : 6.86
	W3	pH : 7.04 (Action Level Exceedance) C1 : 7.22 C2 : 6.86

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.6b (Con't)

Date & Time	Location	Parameters
27 July 2012, 07:35 to 08:47 (Mid-Ebb)	W1	pH : 7.12 (Action Level Exceedance) C1 : 7.49 C2 : 6.97
	W2	pH : 7.02 (Action Level Exceedance) C1 : 7.49 C2 : 6.97
	W3	pH : 7.07 (Action Level Exceedance) C1 : 7.49 C2 : 6.97
27 July 2012, 13:15 to 14:28 (Mid-Flood)	W1	pH : 7.31 (Action Level Exceedance) C1 : 7.23 C2 : 6.81
	W2	pH : 7.16 (Action Level Exceedance) C1 : 7.23 C2 : 6.81
	W3	pH : 7.10 (Action Level Exceedance) C1 : 7.23 C2 : 6.81
30 July 2012, 11:13 to 12:27 (Mid-Ebb)	W1	pH : 7.41 (Action Level Exceedance) C1 : 7.27 C2 : 6.95
	W2	pH : 7.19 (Action Level Exceedance) C1 : 7.27 C2 : 6.95
	W3	pH : 7.36 (Action Level Exceedance) C1 : 7.27 C2 : 6.95
01 Aug 2012, 12:36 to 13:51 (Mid-Ebb)	W2	pH : 7.36 (Action Level Exceedance) C1 : 7.44 C2 : 7.02
	W3	pH : 7.31 (Action Level Exceedance) C1 : 7.44 C2 : 7.02
22 Aug 2012, 15:41 to 16:48 (Mid-Ebb)	W2	pH : 7.30 (Action Level Exceedance) C1 : 7.21 C2 : 6.92
	W3	pH : 7.42 (Action Level Exceedance) C1 : 7.21 C2 : 6.92

4.1.6 Review of the Events Non-compliance

4.1.6.1 Marine Water Quality Monitoring

2 events of exceedance of aluminium were recorded at mid-ebb on 25 July 2012 at M1. Since the pre-bore operation for sheet piling has not commenced yet, so that the exceedance was not caused by the construction work. Heavy rainstorm occurred in the morning, the seabed sediment was stirred up by rainstorm also contributed to the aluminium level at M1. The marine water quality monitoring conducted on 27 July 2012 indicated that the aluminium content returned to <20 µg/L. No potential source

Ref No.: 100440EN120861

of impact was identified and hence, the exceedance should not be related to the Project.

4.1.6.2 Stream Water Quality Monitoring

Construction works, include waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, and glass and steel installation were in progress throughout the reporting period at the North part of the Lagoon and far away from the Tsang Kok Stream. The stream water quality was at the similar level as that before the piling work.

15 events of exceedance of pH were recorded at mid-ebb or mid-flood during August at various locations. The events were recorded at W1, W2 and W3 due to the influence of low pH from upstream of the Tsang Kok stream, heavy rainstorm occurred in 27 July 2012, soil and other runoff were flushed into the river, and rainwater with pH near 7.0 caused the pH at W1, W2 and W3 dropped to below 7.55 and not owing to construction activities related.

The exceedances of pH were unrelated to the construction works, hence the ad-hoc monitoring was cancelled.

The Incident Report on Action and Limit Level Non-compliance is attached in Appendix 9.

4.2 Landfill Gas Monitoring

4.2.1 Monitoring methodology

4.2.1.1 Routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters into the area.

4.2.1.2 For excavations deeper than 1m measurements should be carried out:

- at the ground surface before excavation commences;
- immediately before any worker enters the excavation;
- at the beginning of each working day for the entire period the excavation remains open; and
- periodically through out the working day whilst workers are in the excavation.

4.2.1.3 For excavations between 300mm and 1m deep, measurements should be carried out:

- directly after the excavation has been completed; and

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

- periodically whilst the excavation remains open.

4.2.1.4 For excavations less than 300mm and 1m deep, monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person.

4.2.1.5 Depending on the results of the measurements, actions required will vary and should be set down by the Safety Officer or other appropriately qualified person. As a minimum these should encompass those actions specified in Table 3.4.

4.2.2 Monitoring equipment

Table 4.7 Landfill Gas Monitoring Equipment

Equipment	Model	Parameters Measured
<i>Fieldwork – Landfill Gas Monitoring</i>		
Landfill Gas Analyzer	RAE QRAE II Multi-gas Detector	Methane, oxygen, carbon dioxide

4.2.3 Monitoring result

Excavation works has been carried out within the WENT landfill consultation zone for the following construction activities during the reporting period: (1) Portion 1 (next to Plant B, foundations works for east marshalling area); (2) Portion 3 (next to Canteen, cable ducting) and Portion 3 (next to T758). The excavation depth is more than 1m, and landfill gas monitoring was conducted by a competent person according to methodology stated in section 4.2.1. Monitoring results are tabulated in Table 4.8.

Table 4.8 Summary of Landfill Gas Monitoring during the Reporting Period

Sample Location	Date of Measurement	Sampling Time	Weather Condition	Oxygen %	Methane %LEL	Carbon Dioxide %
Potion 1 (next to Plant B)	26-Jul-12	08:23	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	26-Jul-12	13:16	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	27-Jul-12	08:27	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	27-Jul-12	13:21	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	28-Jul-12	08:22	Fine	20.8	0	0
Potion 1 (next to Plant B)	28-Jul-12	13:17	Fine	20.8	0	0
Potion 1 (next to Plant B)	30-Jul-12	08:30	Sunny	20.9	0	0
Potion 1 (next to Plant B)	30-Jul-12	13:36	Sunny	20.9	0	0
Potion 1 (next to Plant B)	31-Jul-12	08:22	Sunny	20.8	0	0
Potion 1 (next to Plant B)	31-Jul-12	13:16	Sunny	20.8	0	0
Potion 1 (next to Plant B)	01-Aug-12	08:24	Sunny	20.9	0	0
Potion 1 (next to Plant B)	01-Aug-12	13:15	Sunny	20.9	0	0
Potion 1 (next to Plant B)	02-Aug-12	08:17	Sunny	20.8	0	0
Potion 1 (next to Plant B)	02-Aug-12	13:21	Sunny	20.8	0	0
Potion 1 (next to Plant B)	03-Aug-12	08:18	Sunny	20.9	0	0
Potion 1 (next to Plant B)	03-Aug-12	13:17	Sunny	20.9	0	0
Potion 1 (next to Plant B)	04-Aug-12	08:16	Sunny	20.9	0	0
Potion 1 (next to Plant B)	04-Aug-12	13:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	06-Aug-12	08:27	Sunny	20.9	0	0
Potion 1 (next to Plant B)	06-Aug-12	13:22	Sunny	20.9	0	0
Potion 1 (next to Plant B)	07-Aug-12	08:30	Sunny	20.9	0	0
Potion 1 (next to Plant B)	07-Aug-12	13:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	08-Aug-12	08:24	Sunny	20.9	0	0
Potion 1 (next to Plant B)	08-Aug-12	13:15	Sunny	20.9	0	0

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

Table 4.8 (Con't)

Sample Location	Date of Measurement	Sampling Time	Weather Condition	Oxygen %	Methane %LEL	Carbon Dioxide %
Potion 1 (next to Plant B)	09-Aug-12	08:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	09-Aug-12	13:37	Sunny	20.9	0	0
Potion 1 (next to Plant B)	10-Aug-12	08:24	Fine	20.9	0	0
Potion 1 (next to Plant B)	10-Aug-12	13:18	Fine	20.9	0	0
Potion 1 (next to Plant B)	11-Aug-12	08:17	Fine	20.9	0	0
Potion 1 (next to Plant B)	11-Aug-12	13:13	Fine	20.9	0	0
Potion 1 (next to Plant B)	13-Aug-12	08:19	Fine	20.9	0	0
Potion 1 (next to Plant B)	13-Aug-12	13:14	Fine	20.9	0	0
Potion 1 (next to Plant B)	14-Aug-12	08:15	Sunny	20.9	0	0
Potion 1 (next to Plant B)	14-Aug-12	13:14	Sunny	20.9	0	0
Potion 1 (next to Plant B)	15-Aug-12	08:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	15-Aug-12	13:11	Sunny	20.9	0	0
Potion 1 (next to Plant B)	16-Aug-12	08:17	Fine	20.9	0	0
Potion 1 (next to Plant B)	16-Aug-12	13:16	Fine	20.9	0	0
Potion 1 (next to Plant B)	17-Aug-12	08:16	Sunny	20.9	0	0
Potion 1 (next to Plant B)	17-Aug-12	13:17	Sunny	20.9	0	0
Potion 1 (next to Plant B)	18-Aug-12	08:19	Sunny	20.9	0	0
Potion 1 (next to Plant B)	18-Aug-12	13:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	20-Aug-12	08:17	Sunny	20.9	0	0
Potion 1 (next to Plant B)	20-Aug-12	13:19	Sunny	20.9	0	0
Potion 1 (next to Plant B)	21-Aug-12	08:20	Sunny	20.9	0	0
Potion 1 (next to Plant B)	21-Aug-12	13:14	Sunny	20.9	0	0
Potion 1 (next to Plant B)	22-Aug-12	08:17	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	22-Aug-12	13:19	Cloudy	20.9	0	0
Potion 1 (next to Plant B)	23-Aug-12	08:16	Sunny	20.9	0	0
Potion 1 (next to Plant B)	23-Aug-12	13:21	Sunny	20.9	0	0
Potion 1 (next to Plant B)	24-Aug-12	08:40	Sunny	20.9	0	0
Potion 1 (next to Plant B)	24-Aug-12	13:16	Sunny	20.9	0	0
Potion 3 (next to canteen)	26-Jul-12	08:29	Cloudy	20.9	0	0
Potion 3 (next to canteen)	26-Jul-12	13:28	Cloudy	20.9	0	0
Potion 3 (next to canteen)	27-Jul-12	08:44	Cloudy	20.9	0	0
Potion 3 (next to canteen)	27-Jul-12	13:39	Cloudy	20.9	0	0
Potion 3 (next to canteen)	28-Jul-12	08:38	Fine	20.8	0	0
Potion 3 (next to canteen)	28-Jul-12	13:37	Fine	20.8	0	0
Potion 3 (next to canteen)	30-Jul-12	08:47	Sunny	20.9	0	0
Potion 3 (next to canteen)	30-Jul-12	13:52	Sunny	20.9	0	0
Potion 3 (next to canteen)	31-Jul-12	08:36	Sunny	20.8	0	0
Potion 3 (next to canteen)	31-Jul-12	13:34	Sunny	20.8	0	0
Potion 3 (next to canteen)	01-Aug-12	08:36	Sunny	20.9	0	0
Potion 3 (next to canteen)	01-Aug-12	13:24	Sunny	20.9	0	0
Potion 3 (next to canteen)	02-Aug-12	08:27	Sunny	20.8	0	0
Potion 3 (next to canteen)	02-Aug-12	13:29	Sunny	20.8	0	0
Potion 3 (next to canteen)	03-Aug-12	08:27	Sunny	20.9	0	0
Potion 3 (next to canteen)	03-Aug-12	13:29	Sunny	20.9	0	0
Potion 3 (next to canteen)	04-Aug-12	08:27	Sunny	20.9	0	0
Potion 3 (next to canteen)	04-Aug-12	13:36	Sunny	20.9	0	0
Potion 3 (next to canteen)	06-Aug-12	08:39	Sunny	20.9	0	0
Potion 3 (next to canteen)	06-Aug-12	13:29	Sunny	20.9	0	0
Potion 3 (next to canteen)	07-Aug-12	08:39	Sunny	20.9	0	0
Potion 3 (next to canteen)	07-Aug-12	13:32	Sunny	20.9	0	0
Potion 3 (next to canteen)	08-Aug-12	08:29	Sunny	20.9	0	0
Potion 3 (next to canteen)	08-Aug-12	13:24	Sunny	20.9	0	0
Potion 3 (next to canteen)	09-Aug-12	08:27	Sunny	20.9	0	0
Potion 3 (next to canteen)	09-Aug-12	13:24	Sunny	20.9	0	0

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

GEN01/0312

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

Table 4.8 (Con't)

Sample Location	Date of Measurement	Sampling Time	Weather Condition	Oxygen %	Methane %LEL	Carbon Dioxide %
Potion 3 (next to canteen)	10-Aug-12	08:31	Fine	20.9	0	0
Potion 3 (next to canteen)	10-Aug-12	13:24	Fine	20.9	0	0
Potion 3 (next to canteen)	11-Aug-12	08:26	Fine	20.9	0	0
Potion 3 (next to canteen)	11-Aug-12	13:25	Fine	20.9	0	0
Potion 3 (next to canteen)	13-Aug-12	08:24	Fine	20.9	0	0
Potion 3 (next to canteen)	13-Aug-12	13:22	Fine	20.9	0	0
Potion 3 (next to canteen)	14-Aug-12	08:24	Sunny	20.9	0	0
Potion 3 (next to canteen)	14-Aug-12	13:36	Sunny	20.9	0	0
Potion 3 (next to canteen)	15-Aug-12	08:34	Sunny	20.9	0	0
Potion 3 (next to canteen)	15-Aug-12	13:21	Sunny	20.9	0	0
Potion 3 (next to canteen)	16-Aug-12	08:28	Fine	20.9	0	0
Potion 3 (next to canteen)	16-Aug-12	13:24	Fine	20.9	0	0
Potion 3 (next to canteen)	17-Aug-12	08:28	Sunny	20.9	0	0
Potion 3 (next to canteen)	17-Aug-12	13:29	Sunny	20.9	0	0
Potion 3 (next to canteen)	18-Aug-12	08:27	Sunny	20.9	0	0
Potion 3 (next to canteen)	18-Aug-12	13:33	Sunny	20.9	0	0
Potion 3 (next to canteen)	20-Aug-12	08:26	Sunny	20.9	0	0
Potion 3 (next to canteen)	20-Aug-12	13:26	Sunny	20.9	0	0
Potion 3 (next to canteen)	21-Aug-12	08:34	Sunny	20.9	0	0
Potion 3 (next to canteen)	21-Aug-12	13:26	Sunny	20.9	0	0
Potion 3 (next to canteen)	22-Aug-12	08:24	Cloudy	20.9	0	0
Potion 3 (next to canteen)	22-Aug-12	13:29	Cloudy	20.9	0	0
Potion 3 (next to canteen)	23-Aug-12	08:29	Sunny	20.9	0	0
Potion 3 (next to canteen)	23-Aug-12	13:35	Sunny	20.9	0	0
Potion 3 (next to canteen)	24-Aug-12	08:49	Sunny	20.9	0	0
Potion 3 (next to canteen)	24-Aug-12	13:27	Sunny	20.9	0	0
Potion 3 (next to T758)	26-Jul-12	08:34	Cloudy	20.9	0	0
Potion 3 (next to T758)	26-Jul-12	13:36	Cloudy	20.9	0	0
Potion 3 (next to T758)	27-Jul-12	08:39	Cloudy	20.9	0	0
Potion 3 (next to T758)	27-Jul-12	13:32	Cloudy	20.9	0	0
Potion 3 (next to T758)	28-Jul-12	08:31	Fine	20.8	0	0
Potion 3 (next to T758)	28-Jul-12	13:29	Fine	20.8	0	0
Potion 3 (next to T758)	30-Jul-12	08:41	Sunny	20.9	0	0
Potion 3 (next to T758)	30-Jul-12	13:49	Sunny	20.9	0	0
Potion 3 (next to T758)	31-Jul-12	08:29	Sunny	20.8	0	0
Potion 3 (next to T758)	31-Jul-12	13:27	Sunny	20.8	0	0
Potion 3 (next to T758)	01-Aug-12	08:41	Sunny	20.9	0	0
Potion 3 (next to T758)	01-Aug-12	13:29	Sunny	20.9	0	0
Potion 3 (next to T758)	02-Aug-12	08:35	Sunny	20.8	0	0
Potion 3 (next to T758)	02-Aug-12	13:36	Sunny	20.8	0	0
Potion 3 (next to T758)	03-Aug-12	08:36	Sunny	20.9	0	0
Potion 3 (next to T758)	03-Aug-12	13:34	Sunny	20.9	0	0
Potion 3 (next to T758)	04-Aug-12	08:34	Sunny	20.9	0	0
Potion 3 (next to T758)	04-Aug-12	13:43	Sunny	20.9	0	0
Potion 3 (next to T758)	06-Aug-12	08:43	Sunny	20.9	0	0
Potion 3 (next to T758)	06-Aug-12	13:33	Sunny	20.9	0	0
Potion 3 (next to T758)	07-Aug-12	08:46	Sunny	20.9	0	0
Potion 3 (next to T758)	07-Aug-12	13:39	Sunny	20.9	0	0
Potion 3 (next to T758)	08-Aug-12	08:34	Sunny	20.9	0	0
Potion 3 (next to T758)	08-Aug-12	13:36	Sunny	20.9	0	0
Potion 3 (next to T758)	09-Aug-12	08:37	Sunny	20.9	0	0
Potion 3 (next to T758)	09-Aug-12	13:36	Sunny	20.9	0	0
Potion 3 (next to T758)	10-Aug-12	08:39	Fine	20.9	0	0
Potion 3 (next to T758)	10-Aug-12	13:39	Fine	20.9	0	0

Ref No.: 100440EN120861

Table 4.8 (Con't)

Sample Location	Date of Measurement	Sampling Time	Weather Condition	Oxygen %	Methane %LEL	Carbon Dioxide %
Potion 3 (next to T758)	11-Aug-12	08:39	Fine	20.9	0	0
Potion 3 (next to T758)	11-Aug-12	13:38	Fine	20.9	0	0
Potion 3 (next to T758)	13-Aug-12	08:36	Fine	20.9	0	0
Potion 3 (next to T758)	13-Aug-12	13:37	Fine	20.9	0	0
Potion 3 (next to T758)	14-Aug-12	08:39	Sunny	20.9	0	0
Potion 3 (next to T758)	14-Aug-12	13:42	Sunny	20.9	0	0
Potion 3 (next to T758)	15-Aug-12	08:39	Sunny	20.9	0	0
Potion 3 (next to T758)	15-Aug-12	13:27	Sunny	20.9	0	0
Potion 3 (next to T758)	16-Aug-12	08:32	Fine	20.9	0	0
Potion 3 (next to T758)	16-Aug-12	13:29	Fine	20.9	0	0
Potion 3 (next to T758)	17-Aug-12	08:33	Sunny	20.9	0	0
Potion 3 (next to T758)	17-Aug-12	13:36	Sunny	20.9	0	0
Potion 3 (next to T758)	18-Aug-12	08:32	Sunny	20.9	0	0
Potion 3 (next to T758)	18-Aug-12	13:37	Sunny	20.9	0	0
Potion 3 (next to T758)	20-Aug-12	08:34	Sunny	20.9	0	0
Potion 3 (next to T758)	20-Aug-12	13:30	Sunny	20.9	0	0
Potion 3 (next to T758)	21-Aug-12	08:37	Sunny	20.9	0	0
Potion 3 (next to T758)	21-Aug-12	13:32	Sunny	20.9	0	0
Potion 3 (next to T758)	22-Aug-12	08:29	Cloudy	20.9	0	0
Potion 3 (next to T758)	22-Aug-12	13:33	Cloudy	20.9	0	0
Potion 3 (next to T758)	23-Aug-12	08:35	Sunny	20.9	0	0
Potion 3 (next to T758)	23-Aug-12	13:40	Sunny	20.9	0	0
Potion 3 (next to T758)	24-Aug-12	08:55	Sunny	20.9	0	0
Potion 3 (next to T758)	24-Aug-12	13:32	Sunny	20.9	0	0

4.3 Ecological Monitoring

4.3.1 Two monitoring visits were conducted on 08 and 21 August 2012 to assess the measures in place to minimise the disturbance impact to wildlife. The 3m high hoarding to reduce disturbance impact of human activities on adjacent areas (namely the Middle Lagoon and other natural habitats) remains in place. No observations of disturbance through construction operations to wildlife on adjacent habitats were made during this and the other monitoring checks conducted during this period.

4.3.2 Monthly monitoring of avifauna and their notable behaviour, such as breeding activities in the Middle Lagoon, was conducted on 21 August 2012. The Monitoring Area included the whole Middle Lagoon and area extending 20m from the boundary of the Lagoon (see figure 4.1). All birds seen and heard were identified and counted. Any signs of breeding (e.g. nests, recently fledged juveniles) of birds (e.g. Little Grebe) were also recorded. The coverage of water and PFA filling activities in the Middle Lagoon as well as construction activities were also recorded as reference information.

4.3.3 The list of bird surveys recorded from the survey conducted on 21 August 2012 can be seen in Table 4.9. On that date, water coverage in the Middle Lagoon was approximately 90%. No PFA filling activities were recorded in the Middle Lagoon. Nineteen Little Grebes were recorded in the Middle Lagoon, at least 100m from the active construction site. Two juvenile grebes and three nests were also observed.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.9 Bird Species Observed During Monthly Monitoring Surveys in August 2012

Survey Date: 21 August 2012			
Water Levels: 90%			
Species Name	Scientific Name	Middle Lagoon	Breeding Activity
Little Grebe	<i>Tachybaptus ruficollis</i>	19	Three nests seen. Total numbers includes at least 2 juvenile birds.
Little Egret	<i>Egretta garzetta</i>	38	None observed
Black-winged Stilt	<i>Himantopus himantopus</i>	1	None observed
Little Ringed Plover	<i>Charadrius dubius</i>	4	None observed
Wood Sandpiper	<i>Tringa glareola</i>	3	None observed
Greater Coucal	<i>Centropus sinensis</i>	1	None observed
Barn Swallow	<i>Hirundo rustica</i>	20	None observed
Yellow Wagtail	<i>Motacilla flava</i>	12	None observed
White Wagtail	<i>Motacilla alba</i>	8	None observed
Red-Whiskered Bulbul		10	None observed
Plain Prinia		1	None observed
Japanese White-eye	<i>Zosterops japonicus</i>	8	None observed
Crested Myna	<i>Acridotheres cristatellus</i>	4	None observed
Black Drongo	<i>Dicrurus macrocercus</i>	3	None observed
Total Numbers		132	
Total Species		14	

4.4 Landscape and Visual Impact Monitoring

The landscape and visual impact assessment of the EIA Study recommended a series of mitigation measures to ameliorate the landscape and visual impacts of the Project. The measures for the construction phase as recommended in the EIA Report are summarized in Table 4.10.

Site inspections for the monthly EM&A Record for Landscape and Visual Impact (Aug 2012) were undertaken on 06 and 20 of August 2012. Observation of the implementation of proposed landscape and visual mitigation measures are summarized in Table 4.10.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

Table 4.10 Record of Implementation of the Proposed Landscape and Visual Mitigation Measures in Construction Phase (August 2012)

ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status (August 2012)	Remarks
CM1	Design / Construction Planning	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Not applicable.	The topsoil was PFA which is not suitable for re-use in the soft landscape works. Suitable topsoil will be imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of PFA treatment has been shown in Table 4.11.
CM2	Site Practice	Existing trees to be retained on site should be carefully protected during construction.	Tree felling work has commenced since the approval of Phase II tree felling application. Existing trees to be retained have been carefully protected during construction. The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application will be submitted.	Photographic records of the retained trees and T758 are shown in Table 4.11.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

Table 4.10 (Con't)

ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status (August 2012)	Remarks
CM3	Design / Construction Planning	Trees unavoidably affected by the works should be transplanted where practical.	Tree transplant work has been completed. The final transplant locations for the transplant trees will be revised. The transplant trees will be accommodated within the site area. Amendment to the tree felling application will be submitted accordingly.	Tree damages report by Typhoon Vicente on 24 July 2012 has been submitted and 3 transplant trees are reported dead and 1 tree is reported in poor health. The compensatory proposal will be revised in the amendment. The contractor verified on site to ensure the final location of the transplant trees will be suitable for the remaining 13 transplanted trees.
CM4	Design / Construction Planning	Compensatory tree planting should be provided to compensate for felled trees.	Part of the future compensatory trees on the northern seashore are found to be in contradiction with the existing asbestos pipe. Contractor to confirm the removal of the asbestos pipe to accommodate the future compensatory trees. New trees planting is proposed on the either side of the bridge at portion 6 to fulfil the EIA requirements. These shall be reflected in the revised compensatory proposal as well.	The contractor to confirm the schedule for the removal of asbestos pipe as shown in Table 4.11.
CM5	Site Practice	Control of night-time lighting.	In progress.	Night-time work was implemented from 7pm to 6am for certain period in Aug 2012. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.11.

Ref No.: 100440EN120861

Table 4.10 (Con't)

ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status (August 2012)	Remarks
CM6	Design / Construction Planning	Erection of decorative screen hoarding compatible with the surrounding setting.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.

CM1 - Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.

Topsoil found within the project site is PFA, which consist of heavy metals and toxic contaminants that it is not suitable to be re-used as soil mix for landscape softwork. Suitable topsoil will be imported for planting during landscape planting phase. All PFA excavated during the tree felling works has been retained in the site confinement. The PFA has been under dehydration and concealed properly to prevent spreading in the air. Backfill of PFA to its original location inside site boundary is under progress.

CM2 - Existing trees to be retained on site should be carefully protected during construction.

The Tree felling work approved under the Phase 1 and 2 tree felling application has been completed. Proper procedures of tree felling have been observed. The tree felling works should not cause damages to the existing trees on site. The protective tree fence has been established for the retained trees, and some of the broken branches should be removed to avoid further damages. Photographic records of the retained trees are shown in Table 4.11. T758 has been confirmed to be retained on site. Proper tree protection should be set up for T758.

CM3 - Trees unavoidably affected by the works should be transplanted where practical.

Tree transplant works for Tree number T332 to T359 has been completed and proper tree transplant procedure has been observed according to the method statement. The final location of the transplant trees are found in contradiction with the rocky shore area. The transplanted trees will be relocated within the site. This will be reflected in the next tree felling application amendment.

CM4 - Compensatory tree planting should be provided to compensate for felled trees.

Compensatory tree planting has been proposed to and approved by DLO in Phase II tree felling application. The compensatory tree planting has been incorporated with the details of the landscape master plan. Part of the compensatory trees on the northern seashore are found in contradiction with the existing asbestos pipe. Contractor to confirm removal of the asbestos pipe to accommodate the compensatory planting.

New trees planting is proposed on the either side of the bridge at portion 6.

CM5 - Control of night-time lighting.

Night time work was implemented from 7pm to 11pm for certain period in Aug 2012. The lighting is confined to the construction site without affecting the periphery area.

CM6 - Erection of decorative screen hoarding compatible with the surrounding setting.

Construction of decorative screen hoarding compatible with the surrounding setting has been set up in January 2011.

Ref No.: 100440EN120861

Table 4.11 Photographic Record of Landscape and Visual Impact Survey

1. Photographic Record of the PFA Treatment	
	
<p>The PFA excavated has been dehydrated under sunlight, and will be buried back to its original position inside the site boundary.</p>	<p>Capping of the PFA is established to prevent spreading in air.</p>
2. Photographic Record of Protection to the Fell / Retained Trees	
	
<p>The retained trees are in satisfactory condition.</p>	<p>T758 is confirmed to be retained on site. Proper tree protection should be applied to protect T758. Amendment to the tree felling application will be submitted.</p>

Ref No.: 100440EN120861

Table 4.11 (Con't)

3. Photographic Record of the Original Transplant Trees Location




The final location of the transplant trees are found to be in contradiction with the rocky shore. Transplant trees will be relocated within the site and the new tree plantings will be proposed on the either side of the bridge at portion 6 to fulfil the EIA requirement.

4. Photographic Record of the Compensatory Tree Locations



Some of the compensatory trees on the northern seashore are found in contradiction with the existing asbestos pipe. Contractor to confirm the removal of the asbestos pipe to accommodate the compensatory planting.

5. Photographic Record of the Night-Time Working

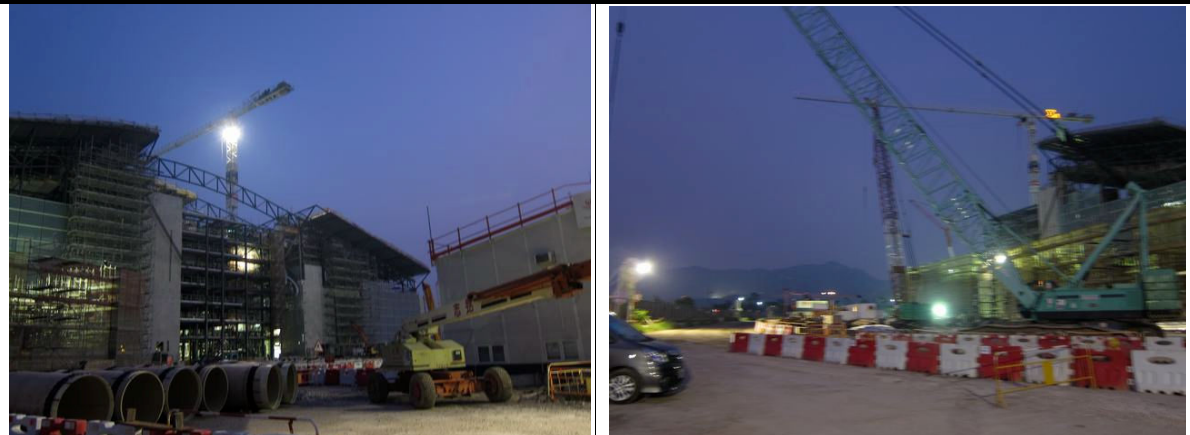

The lighting during night-time working is confined within the working area within the site boundary. Periphery area and the sensitive receivers are not affected by the lighting during night-time working.

The lighting during night-time working is confined within the working area within the site boundary. Periphery area and the sensitive receivers are not affected by the lighting during night-time working.

Ref No.: 100440EN120861

5. Construction Site Environmental Audit**Site Audit**

Site audit is necessary to ensure:

- No unacceptable practice on site;
- Identification of potential impacts associated with construction activities; and
- Implementation of additional mitigation measures if necessary.

Environmental Site Audit has been conducted on 27 July, 03, 10, 17 and 23 August 2012.

During the reporting period, as far as the site operation was concerned, waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, and glass and steel installation were in progress.

Regarding the air quality, access road were watered regularly by water truck or water sprinklers. Most of the site area has been covered by backfill material or coarse asphalt / aggregate. Moisture content of backfill materials and PFA stockpile had to be kept at the designed level before backfilling operation. Contractor should follow the good site practice to minimize the pulverized fuel ash from blowing up from dried surface.

With respect to water quality monitoring, one temporary water detention basin has been constructed at the North of the Lagoon near the ER's office (the east water detention basin has been backfilled). If there is any wastewater generated which will be pumped into the basin and will not be discharged out of the site. Construction of drainage system is in progress.

Major Observation of Site Audit

- The contractor is reminded to increase the frequency of watering on unpaved site roads within the site and properly cover the exposed slope with tarpaulin sheeting.

Waste Management

C&D Waste Backfill and excavation works were conducted during the reporting period. C&D waste was generated from the current activities and sent to public fill.

General Refuse Paper / cardboard, metal and plastics were collected by recycling collectors as far as practicable and general refuse was collected and sent to WENT Landfill.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Ref No.: 100440EN120861

Chemical Waste No chemical waste was generated during the reporting period.

Wastewater Rain water was treated by the silt removal facilities before discharged outside the site. Waste was collected by licensed collector.

Table 5.1 Waste Flow Summary

Type of Waste	Quantity Generated in August 2012	Cumulative quantity during construction period
Inert C&D waste*	1,524.563m ³	13,353.197m ³
Chemical waste (Liquid)	400.000 L	600.000 L
Chemical waste (Solid)	NIL	24,315.000kg
Metal	486,400.000kg	1,684,208.918kg
Paper / Cardboard Packaging	780.000kg	19,956.000kg
Plastic	494.000kg	1,059.000kg
Others, e.g. general refuse	182.556m ³	2,289.513m ³

Remarks: Density of Inert C&D waste and general refuse is 1.9 tonne/m³ and 1.6 tonne/m³ respectively
* The total quantity generated of Inert C&D Waste in April 2012 and May 2012 were revised as the quantities of reused in other projects need to be included

Impact Predication Review

In September 2012, waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, glass and steel installation, pipe Jacking, cable laying, and Condenser Installation will be conducted. It is expected that these operations will not impose significant air, noise and water quality impact to the sensitive receivers. Nevertheless, necessary mitigation measures should be deployed when needed.

FUGRO TECHNICAL SERVICES LIMITEDFugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Ref No.: 100440EN120861

6. Summary of Complaints, Summons and Successful Prosecutions

No complaints, summons and successful prosecutions in association with the construction activities concerning the environmental protection and pollution control were received in the reporting period.

Table 6.1 Summary of Environmental Complaints and Prosecutions

Complaints Logged		Summons Served		Successful Prosecution	
August 2012	Cumulative	August 2012	Cumulative	August 2012	Cumulative
0	1	0	0	0	0

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Ref No.: 100440EN120861

7. Works Program for September 2012

The following major construction works will be in progress in September 2012:

1. Waterproofing;
2. Steel Works;
3. Strut Erection;
4. Substructure Works: Reinforcement, Formwork, Concreting;
5. Structure Works: Reinforcement, Formwork, Concreting;
6. Assembly of Boiler;
7. Structural Steel Erection;
8. Roof Installation;
9. Mechanical Installation;
10. Bridge Construction;
11. Heavy Lifting;
12. Façade Installation;
13. Delivery of Heavy Machineries;
14. E & M Installation;
15. Curtain Wall Installation;
16. Gondola Operation;
17. Inter Decoration;
18. Precast Installation;
19. Road Works;
20. Space Truss Installation;
21. Glass and Steel Installation;
22. Pipe Jacking;
23. Cable Laying; and
24. Condenser Installation

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Ref No.: 100440EN120861

8. Monitoring Schedule for September 2012

The monitoring schedule for September 2012 is shown in Table 8.1.

Table 8.1 Monitoring Schedule for September 2012

SUN	MON	TUE	WED	THU	FRI	SAT
19	20 W# M	21	22 W#	23	24 W#	25
26	27 W#	28	29 W#	30	31 W#	01 Sept
02	03 W#	04	05 W#	06	07 W#	08
09	10 W#	11	12 W#	13	14 W#	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

Legend: W – Stream water quality monitoring at C1, C2, W1, W2 and W3. Three days per week.

M – Marine water quality monitoring at DM4, M1 and M2. Three days per week.

- Note:
1. Marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.
 2. Actual monitoring will be subjected to change due to any safety concern or adverse weather condition.
- # Four weeks post monitoring for stream water commenced by 20 August 2012 and ended on 14 September 2012 inclusively.

Ref No.: 100440EN120861

9. Comments and Conclusions for the Reporting Period

In this reporting period, i.e. 25 July to 24 August 2012, waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, and glass and steel installation were in progress. The site activities did not lead to any significant impact to noise, air quality, stream and marine water quality.

There were 17 events of Action / Limit Level exceedance reported from 25 July to 24 August 2012. 2 events of aluminium exceedance were reported in the reporting period, but since the pre-bore operation for sheet piling has not commenced yet, so that the exceedances were not caused by the construction work. 15 events of pH exceedance were reported in the reporting period that was influent by low pH from upstream, heavy rainstorm, and rainwater with pH near 7.0 caused the pH dropped to below 7.55. All the events were not related to the construction activities.

Contractor shall ensure proper site practices to be implemented to avoid any deterioration of the environment around the construction site. Although there is no sensitive receivers for noise and air quality close to the site area, mitigation measures to minimize dust and noise generated from site activities should be enforced.

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, sans-serif font. The text is centered between two thick, horizontal black bars.


Appendix 1

Water Quality Monitoring Location

LOCATIONS OF STREAM
WATER QUALITY MONITORING STATIONS



STATION	DESCRIPTION	EASTING	NORTHING
W1	IMPACT	810639.3	831296.8
W2	MONITORING	810461.6	831243.9
W3	STATION	810323.6	831196.1
C1	CONTROL	810551.0	830864.0
C2	STATION	810125.0	831084.0

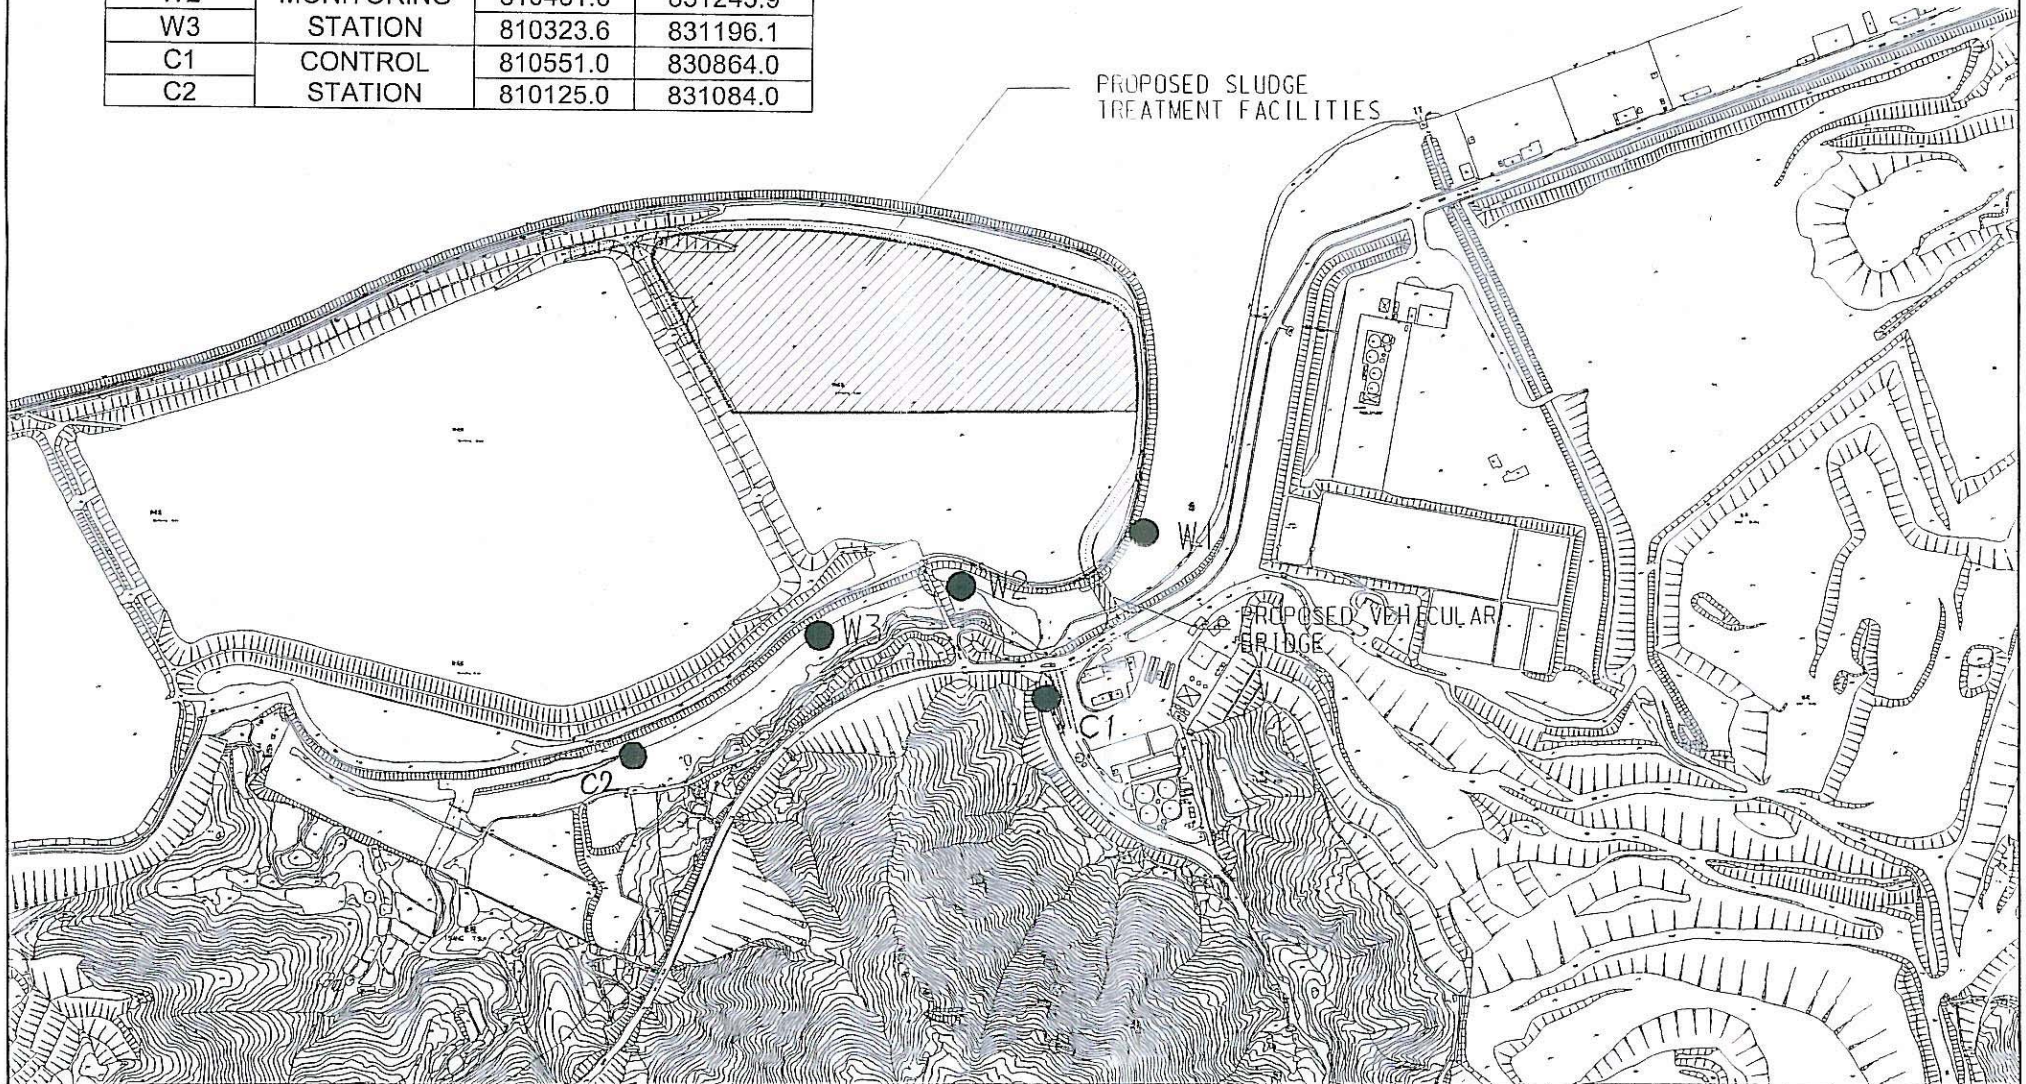

DATE: 8/DATE\$

MAUNSELL | AECOM
Metcalf & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY
LOCATION OF WATER QUALITY MONITORING STATIONS

(Sheet 1 of 2)

SCALE	A3 1:5000	DATE	JUN 2008
CHECK	AKYC	DRAWN	LMWJ
JOB No.	60039510	DRAWING No.	FIGURE 5.1
		REV	-

LOCATIONS OF MARINE
WATER QUALITY MONITORING STATIONS

STATION	EASTING	NORTHING
M1 (IMPACT MONITORING STATION)	809915.3	831971.6
M2 (IMPACT MONITORING STATION)	809026.4	831676.8
DM4 (CONTROL STATION)	811092.2	835181.8



DATE: 5DATE 5

MAUNSELL | AECOM
Metcalfe & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY
LOCATION OF WATER QUALITY MONITORING STATIONS

(Sheet 2 of 2)

SCALE	A3 1:30000	DATE	JUN 2008
CHECK	ARYC	DRAWN	LMW1
JOB NO.	60039510	DRAWING NO.	FIGURE 5.1
		REV	-

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 2

Equipment Calibration Certificates

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong

Tel: +852-2450 8233
Fax: +852-2450 6138
E-mail: matlab@fugro.com.hk
Website: www.fugro.com

MaterialLab

Report No. : 921437CA120485(2)

Page 1 of 1

CALIBRATION RECORD OF WHIRLING PSYCHROMETER**Client Supplied Information**

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Calibration Item - Description : Whirling psychrometer
Serial no. : 02586 (Dry Bulb)
02010 (Wet Bulb)
Equipment ID. : E-092-10

Specification limit : According to full checking report no.: 921436CA101642 , Correction at 25.0°C.

Shall be Within -0.3 °C and +0.7 °C for dry bulb, -0.3 °C and +0.7 °C for wet bulb.

Laboratory Information

Calibrating Equipment - Description : Reference thermometer
Equipment ID. : R-053-5

Date of Calibration : 22-Mar-2012 Ambient Temperature : 22 °C

Calibration location : **Calibration Laboratory of MaterialLab**Method used : **In-house Method R-C-076**In-house testing procedure no. : **R-C-076****Calibration Results :** (All values are in the unit of °C.)

Test temperature	25.0	--	--	--	--
Ref. Thermometer ID.	R-053-5	--	--	--	--
Correction of Ref. Thermometer at test temperature, C	0.06	--	--	--	--
Variation of Ref. Thermometer reading in 20sec.	Maximum	24.96	--	--	--
	Minimum	24.93	--	--	--
Average between Max. & Min., A	24.95	--	--	--	--
Corrected temperature, (A + C), Ra	25.01	--	--	--	--
Dry Bulb	Indicated temperature, Rd	25.0	--	--	--
	Correction, Ra - Rd	0.0	--	--	--
Wet Bulb	Indicated temperature, Rw	24.9	--	--	--
	Correction, Ra - Rw	0.1	--	--	--

Remark :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The discrimination of the equipment under test is 0.1 °C (1/5 division).
3. The equipment being calibrated does comply with the specification limit.
4. Recommended next calibration date (6 months, In-house specification) 22-Sep-2012

Tested by : Edwin M Date : 22 MAR 2012 Checked by : [Signature] Date : 22-3-2012

CA-W-182 (30/07/98)

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

GEN01/0203

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MateriaLab

Report No. : 921438WA120744



Page 1 of 2

Report on Calibration of Professional Plus Water Quality Instrument

Information Supplied by Client

Client : Fugro Technical Services Limited – MateriaLab Division – Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Professional Plus Water Quality Instrument

Client sample ID : Serial No. 10J100270 (E-109-1)

Test required : Calibration of the submitted Professional Plus Water Quality Instrument

Laboratory Information

Lab. sample ID : WA120744/1

Date sample received : 07/05/2012

Date of calibration : 09/05/2012

Next calibration date : 09/08/2012

Test method used : In-house comparison method

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 921438WA120744

Page 2 of 2

Results :**A. Salinity calibration**

Salinity, ‰			
Theoretical	Measured	Deviation	Maximum acceptable Deviation
10	9.96	-0.04	± 0.5
20	20.01	+ 0.01	± 1.0
30	29.98	- 0.02	± 1.5
40	40.11	+ 0.11	± 2.0

B. Dissolved Oxygen calibration


Trial No.	Dissolved oxygen content, mg/L	
	By Titration	By D.O. meter
1	7.77	7.58
2	7.77	7.64
3	7.66	7.62
Average	7.73	7.61

C. Temperature calibration

Thermometer reading, °C	Meter reading, °C
23.5	23.8

D. pH calibration

pH reading at 24°C for Q.C. solution(6.86) and at 24°C for Q.C. solution(9.18)		
Theoretical	Measured	Deviation
9.18	9.18	0.00
6.86	6.88	+ 0.02

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 2/5/2012

** End of Report **

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 921438WA121363



Page 1 of 2

Report on Calibration of Professional Plus Water Quality Instrument

Information Supplied by Client

Client : Fugro Technical Services Limited – Materialab Division –
Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Professional Plus Water Quality Instrument

Client sample ID : Serial No. 10J100270 (E-109-1)

Test required : Calibration of the submitted Professional Plus Water Quality
Instrument

Laboratory Information

Lab. sample ID : WA121363/1

Date sample received : 08/08/2012

Date of calibration : 15/08/2012

Next calibration date : 15/11/2012

Test method used : In-house comparison method

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 921438WA121363

Page 2 of 2

Results :**A. Salinity calibration**

Salinity, ‰			
Theoretical	Measured	Deviation	Maximum acceptable Deviation
10	10.00	0.00	± 0.5
20	20.11	+0.11	± 1.0
30	30.06	+0.06	± 1.5
40	40.12	+0.12	± 2.0

B. Dissolved Oxygen calibration


Trial No.	Dissolved oxygen content, mg/L	
	By Titration	By D.O. meter
1	7.82	7.63
2	7.82	7.60
3	7.82	7.64
Average	7.82	7.62

C. Temperature calibration

Thermometer reading, °C	Meter reading, °C
23.1	23.1

D. pH calibration

pH reading at 22°C for Q.C. solution(6.86) and at 22°C for Q.C. solution(9.18)		
Theoretical	Measured	Deviation
9.18	9.25	+0.07
6.86	6.86	0.00

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 21/8/2012

** End of Report **

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 921438WA121151



Page 1 of 2

REPORT ON CALIBRATION OF TURBIDIMETER

Information Supplied by Client

Client : Fugro Technical Services Limited – Materialab Division – Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Turbidimeter, HACH Model 2100P

Client sample ID : Serial No. 911000304 (E-047- 1)

Test required : Calibration of the submitted Turbidimeter

Laboratory Information

Lab. sample ID : WA121151/1

Date sample received : 04/07/2012

Date of calibration : 06/07/2012

Next calibration date : 06/10/2012

Test method used :

1. Three standard turbidity solutions with 20 NTU, 100 NTU and 800 NTU were prepared.
2. After the blank zero was set, the meter was calibrated against the standard solutions.
3. The gelex secondary standard with 0.00 – 9.99 NTU was inserted and the reading of this gelex standard was recorded. Same steps were repeated for 10 – 99.9 NTU and 100 – 1000 NTU gelex standards.

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 921438WA121151

Page 2 of 2

Results:

Calibrated Values of Secondary Gelex Standards

Auto-programmed Turbidity Standard Range	0.00-9.99 NTU, Gelex Vial	10-99.9 NTU, Gelex Vial	100-1000 NTU, Gelex Vial
Calibrated Value of the Secondary Standard, N.T.U.	5.54	56.1	511

Checking of sample cell condition using filtered ultra-pure water

Turbidity of procedural blank, NTU	
Our sample cell	Client's sample cell
0.13	0.37

- Remarks:
1. Procedural blank of client's sample cell >0.2 NTU, the cell is no longer for low turbidity (<1 NTU) measurement
 2. If the reading of secondary standard was not within $\pm 5\%$ of the calibrated value, the instrument should be recalibrated with formazin primary standards.

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 17/7/2012

** End of Report **

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 921438WA121083



Page 1 of 2

REPORT ON CALIBRATION OF TURBIDIMETER

Information Supplied by Client

Client : Fugro Technical Services Limited – MaterialLab Division – Environmental

Client's address : Fugro Development Centre, 5 Lok Yi St.,
17 M.S. Castle Peak Road, Tuen Mun, N.T.

Project : Routine Calibration

Sample description : One Turbidimeter, HACH Model 2100P

Client sample ID : Serial No. 010800023055(E-047- 3)

Test required : Calibration of the submitted Turbidimeter

Laboratory Information

Lab. sample ID : WA121083/1

Date sample received : 04/07/2012

Date of calibration : 04/07/2012

Next calibration date : 04/10/2012

Test method used :

1. Three standard turbidity solutions with 20 NTU, 100 NTU and 800 NTU were prepared.
2. After the blank zero was set, the meter was calibrated against the standard solutions.
3. The gelex secondary standard with 0.00 – 9.99 NTU was inserted and the reading of this gelex standard was recorded. Same steps were repeated for 10 – 99.9 NTU and 100 – 1000 NTU gelex standards.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 921438WA121083

Page 2 of 2

Results:

Calibrated Values of Secondary Gelex Standards


Auto-programmed Turbidity Standard Range	0.00-9.99 NTU, Gelex Vial	10-99.9 NTU, Gelex Vial	100-1000 NTU, Gelex Vial
Calibrated Value of the Secondary Standard, N.T.U.	5.16	45.3	497

Checking of sample cell condition using filtered ultra-pure water

Turbidity of procedural blank, NTU	
Our sample cell	Client's sample cell
0.25	0.47

- Remarks:
1. Procedural blank of client's sample cell >0.2 NTU, the cell is no longer for low turbidity (<1 NTU) measurement
 2. If the reading of secondary standard was not within $\pm 5\%$ of the calibrated value, the instrument should be recalibrated with formazin primary standards.

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 9/7/2012

** End of Report **

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 3

Stream and Marine Water Quality Monitoring Data

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120860

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 25/07/2012 (p.m.) Test No. : 257
Tide State : MID-EBB Weather : RAINY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:08	25	0.8	25.9	6.3	6.02	77.3	19.4	7.59	14	
				25.8	6.3	5.96	76.6	18.0	7.56	18	
W2	16:27	25.5	0.1	25.2	1.1	6.64	81.9	16.5	7.15	15	
				25.2	1.0	6.61	81.4	15.2	7.08	16	
W3	16:43	25.5	0.7	25.1	0.3	6.79	83.1	13.6	7.08	14	
				25.1	0.3	6.70	82.0	13.2	7.00	16	
C1	17:36	25	0.2	25.0	0.0	7.37	89.9	28.8	7.24	26	
				25.0	0.0	7.27	88.6	29.2	7.20	25	
C2	17:02	25	0.1	25.0	0.2	6.80	83.1	13.3	6.90	15	
				25.0	0.2	6.74	82.4	14.0	6.81	16	

Certified by :



Date :

2/8/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 27/07/2012 (a.m.) Test No. : 258
Tide State : MID-EBB Weather : RAINY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	7:35	25	0.7	26.1	9.0	5.27	70.0	6.43	7.10	6	
				26.1	9.0	5.32	70.6	5.96	7.13	5	
W2	7:54	25	0.1	25.3	2.4	5.84	72.7	9.30	7.03	15	
				25.3	2.4	5.77	71.9	10.1	7.01	13	
W3	8:09	25	0.6	25.0	0.9	6.51	79.8	20.8	7.08	27	
				25.0	0.9	6.47	79.4	19.7	7.05	28	
C1	8:47	25	0.1	24.8	0.0	7.43	90.3	276	7.50	310	
				24.8	0.0	7.45	90.5	280	7.48	250	
C2	8:32	25	0.1	24.8	0.3	5.97	71.4	13.1	6.96	20	
				24.9	0.3	5.90	70.6	13.6	6.98	20	

Certified by :



Approved Signatory : K.M. Ho

Date :

3/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 27/07/2012 (p.m.) Test No. : 258
Tide State : MID-FLOOD Weather : RAINY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:15	25	0.3	26.1	5.0	6.82	87.3	32.5	7.29	27	
				26.1	4.9	6.72	86.0	29.6	7.32	27	
W2	13:38	26	0.1	25.3	0.6	6.91	85.0	14.4	7.20	13	
				25.2	0.7	6.87	84.6	16.0	7.12	16	
W3	13:54	25.5	0.4	25.2	0.3	7.16	87.9	14.3	7.13	14	
				25.2	0.4	7.06	86.6	14.0	7.07	17	
C1	14:28	25	0.1	25.2	0.0	7.67	94.0	88.3	7.22	120	
				25.3	0.0	7.71	94.6	86.9	7.24	140	
C2	14:12	26	0.1	25.0	0.1	7.18	87.7	17.6	6.82	16	
				25.0	0.1	7.10	86.7	17.1	6.80	15	

Certified by :


 Approved Signatory : K.M. Ho

Date :

3/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 30/07/2012 (a.m.) Test No. : 259
Tide State : MID-EBB Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:13	32	0.5	29.5	10.1	6.45	90.4	4.22	7.40	3	
				29.6	10.1	6.40	89.8	4.10	7.42	4	
W2	11:32	32	0.1	29.2	5.4	7.53	102.5	9.23	7.20	10	
				29.2	5.4	7.49	101.9	8.75	7.18	11	
W3	11:49	32	0.1	29.6	3.1	8.24	111.4	12.6	7.37	19	
				29.7	3.1	8.10	109.6	11.2	7.34	20	
C1	12:27	32	0.1	29.3	0.0	9.03	119.4	5.28	7.29	2	
				29.3	0.0	8.92	117.9	5.35	7.24	3	
C2	12:11	32	0.1	28.5	1.2	8.40	110.1	4.90	6.95	4	
				28.5	1.2	8.28	108.8	4.55	6.94	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

6/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 30/07/2012 (p.m.) Test No. : 259
Tide State : MID-FLOOD Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	17:50	33	0.1	31.1	8.7	5.87	84.2	24.4	7.58	29	
				31.1	8.8	5.84	83.8	27.3	7.60	36	
W2	18:10	32	0.1	28.4	1.3	6.54	86.1	30.9	7.64	38	
				28.5	1.4	6.63	87.4	30.5	7.66	30	
W3	18:27	31	0.2	27.6	1.1	6.55	84.9	8.93	7.73	11	
				27.7	1.2	6.49	84.0	9.36	7.75	17	
C1	18:56	30	0.1	27.1	0.0	7.16	91.3	5.39	7.18	3	
				27.0	0.0	7.10	90.7	5.84	7.15	3	
C2	18:42	31	0.1	27.1	0.9	6.09	78.0	5.34	7.20	3	
				27.0	1.0	6.01	77.0	5.12	7.18	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

6/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 01/08/2012 (a.m.) Test No. : 260
Tide State : MID-FLOOD Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	6:53	27	1.0	28.3	14.9	5.25	75.1	4.69	7.61	3	
				28.2	14.9	5.34	76.2	4.26	7.60	3	
W2	7:11	27.5	0.1	28.2	14.0	5.42	76.9	6.52	7.59	7	
				28.2	13.9	5.45	77.2	6.86	7.60	8	
W3	7:26	27.5	1.0	28.2	13.2	5.24	73.9	6.93	7.58	8	
				28.2	13.2	5.20	73.4	6.74	7.59	7	
C1	7:57	28	0.1	26.0	0.0	8.57	107.2	15.5	7.43	12	
				26.0	0.0	8.53	106.7	14.3	7.41	10	
C2	7:42	28	0.1	27.9	11.9	5.65	76.9	7.47	7.56	7	
				27.8	11.8	5.60	76.4	7.20	7.56	6	

Certified by :



Approved Signatory : K.M. Ho

Date :

9/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 01/08/2012 (p.m.) Test No. : 260
Tide State : MID-EBB Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	12:36	34	0.8	30.2	14.8	6.04	88.2	4.29	7.66	2	
				30.2	14.8	5.95	87.1	3.90	7.67	3	
W2	12:56	33	0.1	29.9	9.2	6.45	91.1	8.54	7.34	8	
				29.9	9.2	6.34	89.6	7.92	7.37	9	
W3	13:13	33	0.5	29.7	6.3	7.95	110.1	5.60	7.31	8	
				29.8	6.2	7.77	107.7	5.76	7.30	9	
C1	13:51	34	0.1	30.7	0.0	8.74	119.1	17.0	7.45	10	
				30.7	0.0	8.70	118.6	15.8	7.43	11	
C2	13:34	34	0.1	29.0	3.5	7.96	107.2	3.83	7.04	3	
				29.1	3.5	7.84	105.7	3.71	7.00	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

9/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 03/08/2012 (a.m.) Test No. : 261
Tide State : MID-FLOOD Weather : HAZY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	8:17	31	1.0	29.2	12.5	5.19	73.6	5.17	7.55	5	
				29.2	12.7	5.21	73.9	5.26	7.55	5	
W2	9:05	31	0.1	29.1	11.5	5.31	74.7	10.4	7.57	13	
				29.1	11.6	5.34	75.1	10.9	7.58	20	
W3	8:40	31	0.9	29.2	14.1	5.17	73.4	8.22	7.56	9	
				29.3	14.2	5.18	73.6	8.29	7.56	9	
C1	7:38	31	0.1	26.7	0.0	8.05	102.0	4.82	6.70	<1	
				26.7	0.0	8.02	101.7	4.61	6.68	1	
C2	7:58	30	0.1	28.2	7.6	5.92	80.6	4.36	7.23	4	
				28.0	7.8	5.74	77.7	4.24	7.26	4	

Certified by



Approved Signatory : K.M. Ho

Date :

9/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710


Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 03/08/2012 (p.m.) Test No. : 261
Tide State : MID-EBB Weather : HAZY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	14:21	34	0.65	30.1	12.7	5.57	80.4	5.27	7.55	5	Turbid Water
				30.0	12.7	5.59	80.6	4.69	7.55	4	
W2	14:57	34	0.1	29.4	6.8	7.39	102.2	11.50	7.56	15	
				29.2	7.0	7.26	100.3	11.20	7.58	16	
W3	15:20	32	0.2	29.0	5.2	8.32	113.2	10.20	7.56	13	
				28.9	5.4	7.90	106.7	11.00	7.57	15	
C1	13:45	32	0.1	29.2	0.0	8.84	117.3	179.0	7.96	110	
				29.0	0.0	9.10	119.3	188.0	7.90	100	
C2	13:57	32	0.1	28.3	4.2	6.89	92.0	5.56	7.10	6	
				28.1	4.0	6.86	91.5	6.23	7.15	6	

Certified by :  Date : 9/8/2012
Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 06/08/2012 (a.m.) Test No. : 262
Tide State : MID-FLOOD Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:03	30.5	1.0	29.5	13.3	5.21	74.3	7.24	7.60	5	
				29.5	13.3	5.30	75.4	6.98	7.61	6	
W2	10:23	31.5	0.1	29.5	10.4	5.26	73.7	17.2	7.58	18	
				29.5	10.4	5.34	74.6	17.7	7.59	19	
W3	10:38	32	1.0	29.6	10.3	5.40	75.2	20.6	7.60	21	
				29.6	10.3	5.37	74.9	22.6	7.58	20	
C1	11:08	32	0.1	29.0	0.0	8.24	108.2	105	8.14	58	
				29.0	0.0	8.13	106.9	106	8.10	50	
C2	10:54	32	0.1	28.9	7.3	5.76	78.7	11.0	7.42	8	
				29.0	7.2	5.68	77.7	10.0	7.38	9	

Certified by :



Approved Signatory : K.M. Ho

Date :

10/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 06/08/2012 (p.m.) Test No. : 262
Tide State : MID-EBB Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:26	32	0.8	30.4	11.3	5.86	84.1	8.08	7.60	6	
				30.4	11.3	5.77	82.9	7.51	7.60	5	
W2	15:42	31	0.1	29.5	8.2	6.55	91.0	9.63	7.60	10	
				29.5	8.2	6.43	89.4	10.4	7.60	13	
W3	15:56	31	0.5	29.0	4.3	7.82	105.5	6.00	7.70	6	
				29.0	4.4	7.62	102.9	6.09	7.69	6	
C1	16:26	31	0.1	28.5	0.0	7.92	103.5	65.7	7.96	51	
				28.5	0.0	7.87	102.8	70.7	7.89	42	
C2	16:12	30.5	0.1	27.8	2.3	6.72	87.8	4.96	7.34	4	
				27.8	2.3	6.66	87.0	4.63	7.24	4	

Certified by :



Approved Signatory : K.M. Ho

Date :

10/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 08/08/2012 (a.m.) Test No. : 263
Tide State : MID-FLOOD Weather : HAZY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:34	32.5	0.7	31.0	12.6	5.63	81.2	12.8	7.59	13	
				31.0	12.6	5.69	82.1	11.9	7.63	13	
W2	11:52	33	0.1	31.2	11.8	5.78	83.2	17.5	7.66	18	
				31.1	11.8	5.62	80.9	16.9	7.69	17	
W3	12:05	33.5	0.7	31.0	10.2	5.82	82.8	13.5	7.74	12	
				31.0	10.3	5.77	82.1	12.2	7.73	15	
C1	12:40	34	0.1	31.7	0.0	8.36	113.9	8.30	8.40	6	
				31.7	0.0	8.24	112.2	8.76	8.30	6	
C2	12:24	33.5	0.1	30.6	1.0	8.76	117.7	6.81	8.44	4	
				30.6	1.0	8.62	116.0	6.34	8.43	5	

Certified by :



Approved Signatory : K.M. Ho

Date :

14/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 08/08/2012 (p.m.) Test No. : 263
Tide State : MID-EBB Weather : HAZY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:30	35	0.6	31.8	12.2	6.49	94.5	6.37	7.74	6	
				31.8	12.2	6.34	82.4	6.43	7.75	7	
W2	16:52	34	0.1	31.4	9.9	6.99	100.0	16.5	7.87	18	
				31.4	9.9	6.82	97.5	14.7	7.89	21	
W3	17:06	33.5	0.4	31.3	4.7	8.96	124.3	5.47	8.05	6	
				31.0	4.5	8.63	118.7	5.84	8.00	6	
C1	17:37	34	0.1	30.2	0.0	7.64	101.5	16.0	8.23	14	
				30.2	0.0	7.43	98.7	17.4	8.13	16	
C2	17:23	33.5	0.1	29.4	1.1	7.44	98.0	5.92	7.86	6	
				29.4	1.0	7.34	96.6	5.70	7.84	5	

Certified by :



Approved Signatory : K.M. Ho

Date :

14/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 10/08/2012 (a.m.) Test No. : 264
Tide State : MID-EBB Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	7:16	30	0.6	30.3	13.2	5.51	78.7	8.61	7.63	7	
				30.3	13.2	5.56	79.4	8.38	7.64	8	
W2	7:36	30	0.1	29.2	8.1	5.30	73.0	12.8	7.59	15	
				29.2	8.1	5.34	73.4	12.9	7.59	15	
W3	7:51	30.5	0.4	28.7	4.5	5.64	74.8	5.25	7.57	5	
				28.7	4.5	5.52	73.3	4.93	7.56	5	
C1	8:34	31	0.1	27.9	0.0	7.31	93.2	53.5	7.89	42	
				27.9	0.0	7.17	91.4	52.3	7.74	41	
C2	8:11	31	0.1	28.2	1.2	5.92	76.5	4.25	7.30	4	
				28.2	1.2	5.99	77.4	4.10	7.26	4	

Certified by :



Approved Signatory : K.M. Ho

Date :

16/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 10/08/2012 (p.m.) Test No. : 264
Tide State : MID-FLOOD Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:50	32.5	0.4	31.3	13.1	7.04	102.2	24.9	7.76	31	
				31.3	13.1	6.95	101.1	25.4	7.77	29	
W2	14:07	31.5	0.1	32.5	11.5	8.02	117.9	30.8	7.93	31	
				32.5	11.4	7.92	116.3	28.3	7.94	33	
W3	14:21	30	0.4	32.0	2.2	7.32	129.0	15.8	8.04	17	
				32.0	2.1	9.21	127.6	15.7	8.06	16	
C1	14:57	31	0.1	30.6	0.0	7.89	105.5	11.2	8.37	7	
				30.6	0.0	7.72	103.3	10.1	8.30	8	
C2	14:40	30	0.1	29.3	0.5	7.45	97.7	6.04	8.39	6	
				29.3	0.5	7.33	96.1	5.97	8.38	5	

Certified by :



Approved Signatory : K.M. Ho

Date :

16/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 13/08/2012 (a.m.) Test No. : 265
Tide State : MID-EBB Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	10:23	29	0.5	29.4	8.2	5.87	80.4	24.3	7.62	18	
				29.4	8.2	5.89	80.7	22.4	7.65	21	
W2	10:59	29	0.1	28.5	2.7	6.86	89.8	11.7	7.64	16	
				28.5	2.7	6.72	87.9	11.0	7.66	13	
W3	11:13	29.5	0.1	28.5	2.3	7.37	96.2	11.0	7.78	9	
				28.5	2.3	7.24	94.5	10.6	7.80	10	
C1	11:28	30	0.1	28.1	0.0	7.33	93.7	33.6	7.73	20	
				28.1	0.0	7.20	92.1	36.7	7.72	17	
C2	10:44	29	0.1	27.6	0.5	7.87	100.2	10.6	7.76	6	
				27.6	0.5	7.79	99.1	11.0	7.75	6	

Certified by :



Date :

17/8/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Our Ref. No. : 100440EN120710


Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 13/08/2012 (p.m.) Test No. : 265
Tide State : MID-FLOOD Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	17:33	30	0.1	29.9	10.9	6.18	86.7	29.9	7.70	27	
				29.9	10.9	6.06	84.9	26.3	7.71	30	
W2	18:25	29.5	0.1	29.3	2.2	6.35	84.0	14.4	7.87	21	
				29.3	2.2	6.15	81.3	15.0	7.86	20	
W3	18:40	29	0.2	28.4	1.4	5.85	75.9	12.8	7.82	18	
				28.4	1.4	5.90	76.6	14.3	7.80	19	
C1	17:51	29	0.1	28.7	0.0	7.07	91.5	10.1	7.87	6	
				28.7	0.0	6.91	89.5	9.96	7.85	5	
C2	18:06	29	0.1	28.0	0.5	6.28	80.5	11.7	7.60	7	
				28.0	0.5	6.20	79.5	11.2	7.59	7	

Certified by :  Date : 13/8/2012
Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 15/08/2012 (a.m.) Test No. : 266
Tide State : MID-EBB Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:40	33	0.7	31.2	12.5	5.84	84.3	4.75	7.60	4	
				31.2	12.4	5.70	82.4	4.43	7.63	3	
W2	11:59	34	0.1	31.0	9.0	7.00	99.0	10.6	7.73	12	
				31.0	9.0	6.93	98.0	11.2	7.73	12	
W3	12:15	35	0.4	31.3	5.5	8.64	120.5	3.78	7.90	4	
				31.3	5.5	8.54	120.0	3.49	7.89	4	
C1	12:48	34	0.1	33.2	0.0	7.91	110.5	24.9	8.30	9	
				33.2	0.0	7.99	111.8	24.0	8.26	12	
C2	12:34	34	0.1	30.6	2.6	8.38	113.5	4.06	7.97	5	
				30.6	2.5	8.25	111.8	4.33	7.95	15	

Certified by :



Date :

21/8/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 15/08/2012 (p.m.) Test No. : 266
Tide State : MID-FLOOD Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	18:11	33	0.1	31.9	14.4	6.83	100.8	27.4	7.78	32	
				31.8	14.4	6.73	99.5	24.9	7.80	31	
W2	18:36	32	0.1	30.2	3.8	6.14	83.3	11.2	7.90	15	
				30.3	3.8	6.04	82.0	11.4	7.88	14	
W3	18:50	31	0.1	29.4	2.6	5.49	72.8	11.8	7.77	17	
				29.4	2.6	5.60	74.3	12.1	7.73	15	
C1	19:23	30	0.1	29.3	0.0	6.60	86.4	7.77	8.07	4	
				29.3	0.0	6.50	85.0	8.01	8.05	3	
C2	19:08	30	0.1	28.2	0.5	5.74	73.0	4.34	7.72	4	
				28.2	0.5	5.80	73.5	4.44	7.70	3	

Certified by :



Approved Signatory : K.M. Ho

Date :

21/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 17/08/2012 (a.m.) Test No. : 267
Tide State : MID-FLOOD Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	8:29	29	1.4	28.2	19.6	5.27	71.9	4.02	7.73	5	
				28.2	19.8	5.19	70.7	4.35	7.74	5	
W2	7:45	28	0.1	27.6	16.3	5.21	71.0	9.99	7.61	10	
				27.6	16.5	5.22	71.2	11.2	7.63	10	
W3	8:02	28	1.3	27.8	16.1	5.38	74.8	9.42	7.72	8	
				27.6	15.8	5.26	73.3	9.91	7.71	9	
C1	7:08	28	0.1	26.0	0.1	6.80	83.8	38.1	7.33	21	
				26.0	0.1	6.75	83.2	37.0	7.26	19	
C2	7:29	28	0.1	27.0	8.7	4.44	58.5	6.25	7.24	4	
				27.1	8.6	4.47	58.9	5.66	7.25	5	

Certified by :



Approved Signatory : K.M. Ho

Date :

27/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 17/08/2012 (p.m.) Test No. : 267
Tide State : MID-EBB Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:05	30	0.9	29.1	17.3	5.35	76.8	4.56	7.78	5	
				29.0	17.4	5.55	79.4	4.76	7.77	5	
W2	13:25	30	0.1	29.0	12.1	6.31	87.4	12.3	7.70	16	
				28.9	12.1	6.24	86.5	12.0	7.67	15	
W3	13:42	29	0.5	28.7	7.8	6.98	94.1	4.26	7.65	5	
				28.7	7.8	6.96	93.9	5.09	7.64	8	
C1	14:16	30	0.1	29.1	0.1	7.51	97.6	25.0	7.95	20	
				29.1	0.1	7.44	96.9	24.9	7.93	20	
C2	14:00	30	0.1	28.3	4.9	7.17	94.4	3.73	7.44	4	
				28.1	4.8	7.20	94.9	4.15	7.42	5	

Certified by :


 Approved Signatory : K.M. Ho

Date :

27/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 20/08/2012 (a.m.) Test No. : 268
Tide State : MID-FLOOD Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	9:25	32	0.5	29.6	12.5	5.62	75.2	11.9	7.59	10	
				29.7	12.7	5.56	73.9	11.0	7.60	10	
W2	9:46	32	0.1	30.2	13.2	5.65	76.1	14.3	7.64	11	
				30.1	13.2	5.55	73.9	15.1	7.64	12	
W3	10:06	32	0.6	30.1	14.7	5.56	74.8	12.4	7.64	5	
				30.1	14.6	5.65	76.0	11.9	7.64	6	
C1	8:35	30	0.1	27.8	0.1	7.63	97.2	21.2	7.65	14	
				27.8	0.1	7.50	95.6	22.7	7.68	15	
C2	9:00	30	0.1	28.2	4.8	6.34	83.4	7.73	7.56	4	
				28.2	4.9	6.12	80.4	6.97	7.55	4	

Certified by :



Approved Signatory : K.M. Ho

Date :

21/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 20/08/2012 (p.m.) Test No. : 268
Tide State : MID-EBB Weather : SUNNY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	15:22	35	0.3	31.2	13.4	6.22	90.7	9.18	7.79	10	
				31.2	13.3	6.11	89.0	9.40	7.80	10	
W2	15:43	34	0.1	31.4	9.4	8.83	126.3	10.7	7.98	15	
				31.3	9.6	8.85	126.5	9.90	7.99	16	
W3	16:01	34	0.2	30.1	6.4	7.74	106.0	4.64	7.99	13	
				30.0	6.4	7.80	106.9	4.86	7.97	15	
C1	14:45	34	0.1	32.5	0.1	8.09	111.8	16.9	8.01	17	
				32.5	0.1	7.82	108.0	17.0	7.99	16	
C2	15:05	34	0.1	30.6	3.7	8.07	110.2	3.62	7.91	7	
				30.6	3.8	8.30	113.0	3.52	7.91	7	

Certified by :



Approved Signatory : K.M. Ho

Date : 27/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Our Ref. No. : 100440EN120710


Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 22/08/2012 (a.m.) Test No. : 269
Tide State : MID-FLOOD Weather : RAINY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	11:17	26.5	1.0	27.3	6.5	7.13	93.4	86.0	7.64	56	Turbid Water
				27.3	6.5	7.06	92.4	79.8	7.65	49	
W2	10:41	26	0.1	26.2	0.6	8.40	104.3	104	7.61	100	
				26.2	0.7	8.28	102.8	105	7.59	110	
W3	10:56	26	0.9	25.9	0.1	8.57	105.5	108	7.57	90	
				25.9	0.1	8.44	103.9	103	7.58	89	
C1	10:09	26	0.2	25.8	0.0	9.21	113.1	999>	8.32	1900	
				25.8	0.0	9.06	111.3	999>	8.26	1800	
C2	10:24	26	0.1	25.8	0.0	8.78	107.9	133	7.81	140	
				25.9	0.0	8.57	105.3	129	7.58	120	

Certified by :  Date : 27/8/2012
Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 22/08/2012 (p.m.) Test No. : 269
Tide State : MID-EBB Weather : CLOUDY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	16:48	28	0.3	28.3	8.2	5.28	71.0	22.5	7.55	28	
				28.3	8.2	5.34	71.8	26.2	7.56	25	
W2	16:14	28	0.1	27.3	2.5	6.33	81.0	16.1	7.29	16	
				27.3	2.5	6.27	80.2	16.2	7.30	17	
W3	16:29	28	0.4	26.9	1.5	5.92	74.8	10.6	7.42	11	
				26.9	1.5	5.87	74.2	10.2	7.41	11	
C1	15:41	29	0.1	26.6	0.0	7.58	94.4	55.5	7.19	43	
				26.5	0.0	7.41	92.1	52.5	7.23	40	
C2	15:57	28	0.1	26.4	0.6	6.78	84.4	11.8	6.91	12	
				26.4	0.6	6.65	82.8	11.4	6.93	12	

Certified by :



Approved Signatory : K.M. Ho

Date :

27/8/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 24/08/2012 (a.m.) Test No. : 270
Tide State : MID-FLOOD Weather : SUNNY
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	13:32	34	0.6	32.0	12.5	6.53	95.7	13.4	7.70	15	
				32.0	12.5	6.42	94.0	14.1	7.70	13	
W2	12:54	34	0.1	32.5	8.7	6.74	97.4	32.7	7.59	38	
				32.5	8.8	6.58	95.2	29.2	7.63	28	
W3	13:12	34	0.5	33.3	2.9	9.72	138.4	13.4	7.80	16	
				33.3	2.9	9.63	136.9	13.1	7.84	15	
C1	12:21	34	0.1	30.0	0.0	8.85	117.2	17.4	7.41	10	
				30.0	0.0	8.68	114.9	17.2	7.46	11	
C2	12:38	33	0.1	29.9	1.1	9.04	120.0	4.73	7.39	3	
				29.9	1.1	8.91	118.3	4.67	7.48	2	

Certified by :


Approved Signatory : K.M. Ho

Date :

7/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN120710

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Stream Water)

Date : 24/08/2012 (p.m.) Test No. : 270
Tide State : MID-EBB Weather : FINE
Site Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Water Temp. °C	Salinity ppt	D.O. mg/L	D.O.S. %	Turbidity NTU	pH Unit	Suspended Solids Content, mg/L	Remarks
W1	18:18	33	0.4	31.1	10.3	6.61	94.3	9.54	7.79	9	
				31.1	10.3	6.56	93.8	9.29	7.78	11	
W2	17:40	33.5	0.1	31.9	9.8	6.83	98.4	13.9	7.73	18	
				31.9	9.8	6.66	96.0	11.6	7.78	14	
W3	17:55	33	0.4	31.2	4.9	6.79	94.3	5.32	7.81	6	
				31.2	4.9	6.70	93.2	5.13	7.80	5	
C1	17:06	33.5	0.1	29.5	0.0	7.77	102.0	36.3	7.56	21	
				29.5	0.0	7.70	101.0	37.7	7.57	24	
C2	17:22	33	0.1	28.8	0.9	6.97	90.8	4.15	7.20	4	
				28.8	0.9	6.90	89.8	4.03	7.18	3	

Certified by :



Date :

7/9/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Report No. : 100440WA121082(10)



Page 1 of 2



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Ten samples of stream water taken by the staff of MaterialLab on 25/07/2012

Client sample ID :
1. C1 PE
2. C1 PE
3. C2 PE
4. C2 PE
5. W1 PE
6. W1 PE
7. W2 PE
8. W2 PE
9. W3 PE
10. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121082(10)/1 – WA121082(10)/10

Date of receipt of sample : 25/07/2012

Date test commenced : 26/07/2012

Date test completed : 27/07/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121082(10)

Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 PE	26
2. C1 PE	25
3. C2 PE	15
4. C2 PE	16
5. W1 PE	14
6. W1 PE	18
7. W2 PE	15
8. W2 PE	16
9. W3 PE	14
10. W3 PE	16

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 1/8/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121082(10)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
-	-	-

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	99.6

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Report No. : 100440WA121082(11)



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 27/07/2012

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121082(11)/1 – WA121082(11)/20

Date of receipt of sample : 27/07/2012

Date test commenced : 28/07/2012

Date test completed : 30/07/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk


MaterialLab

Report No. : 100440WA121082(11)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	310
2. C1 AE	250
3. C2 AE	20
4. C2 AE	20
5. W1 AE	6
6. W1 AE	5
7. W2 AE	15
8. W2 AE	13
9. W3 AE	27
10. W3 AE	28
11. C1 PF	120
12. C1 PF	140
13. C2 PF	16
14. C2 PF	15
15. W1 PF	27
16. W1 PF	27
17. W2 PF	13
18. W2 PF	16
19. W3 PF	14
20. W3 PF	17

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 3/8/2012

End of Report

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121082(11)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W3 AE	27	27

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	100.6

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Report No. : 100440WA121082(12)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 30/07/2012

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121082(12)/1 – WA121082(12)/20

Date of receipt of sample : 30/07/2012

Date test commenced : 31/07/2012

Date test completed : 01/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121082(12)


Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	2
2. C1 AE	3
3. C2 AE	4
4. C2 AE	3
5. W1 AE	3
6. W1 AE	4
7. W2 AE	10
8. W2 AE	11
9. W3 AE	19
10. W3 AE	20
11. C1 PF	3
12. C1 PF	3
13. C2 PF	3
14. C2 PF	3
15. W1 PF	29
16. W1 PF	36
17. W2 PF	38
18. W2 PF	30
19. W3 PF	11
20. W3 PF	17

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 6/18/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121082(12)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	36	35

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	98.0

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 01/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280/1 – WA121280/20

Date of receipt of sample : 01/08/2012

Date test commenced : 02/08/2012

Date test completed : 03/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab


Report No. : 100440WA121280

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	12
2. C1 AF	10
3. C2 AF	7
4. C2 AF	6
5. W1 AF	3
6. W1 AF	3
7. W2 AF	7
8. W2 AF	8
9. W3 AF	8
10. W3 AF	7
11. C1 PE	10
12. C1 PE	11
13. C2 PE	3
14. C2 PE	3
15. W1 PE	2
16. W1 PE	3
17. W2 PE	8
18. W2 PE	9
19. W3 PE	8
20. W3 PE	9

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 9/8/2012****End of Report*****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
-	-	-

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102.0

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(1)



Page 1 of 2



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of Materialab on 03/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(1)/1 – WA121280(1)/20

Date of receipt of sample : 03/08/2012

Date test commenced : 04/08/2012

Date test completed : 06/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(1)

Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	<1
2. C1 AF	1
3. C2 AF	4
4. C2 AF	4
5. W1 AF	5
6. W1 AF	5
7. W2 AF	13
8. W2 AF	20
9. W3 AF	9
10. W3 AF	9
11. C1 PE	110
12. C1 PE	100
13. C2 PE	6
14. C2 PE	6
15. W1 PE	5
16. W1 PE	4
17. W2 PE	15
18. W2 PE	16
19. W3 PE	13
20. W3 PE	15

Supervised by : Y. M. Chung

Certified by: 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 9/8/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(1)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 PE	16	16

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	101.0

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(2)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture
Client's address : P.O. Box 45, General Post Office, Hong Kong
Project : STF Environmental Team and Independent Environmental
Checker and EM&A Programme
Sample description : Twenty samples of stream water taken by the staff of MaterialLab
on 06/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(2)/1 – WA121280(2)/20
Date of receipt of sample : 06/08/2012
Date test commenced : 07/08/2012
Date test completed : 08/08/2012
Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


MaterialLab

Report No. : 100440WA121280(2)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	58
2. C1 AF	50
3. C2 AF	8
4. C2 AF	9
5. W1 AF	5
6. W1 AF	6
7. W2 AF	18
8. W2 AF	19
9. W3 AF	21
10. W3 AF	20
11. C1 PE	51
12. C1 PE	42
13. C2 PE	4
14. C2 PE	4
15. W1 PE	6
16. W1 PE	5
17. W2 PE	10
18. W2 PE	13
19. W3 PE	6
20. W3 PE	6

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 10/8/2012

End of Report

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(2)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 AF	20	18

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	100.4

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk


Materialab

Report No. : 100440WA121280(3)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	6
2. C1 AF	6
3. C2 AF	4
4. C2 AF	5
5. W1 AF	13
6. W1 AF	13
7. W2 AF	18
8. W2 AF	17
9. W3 AF	12
10. W3 AF	15
11. C1 PE	14
12. C1 PE	16
13. C2 PE	6
14. C2 PE	5
15. W1 PE	6
16. W1 PE	7
17. W2 PE	18
18. W2 PE	21
19. W3 PE	6
20. W3 PE	6

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 14/12/2012****End of Report*****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(3)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
-	-	-

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	99.8

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(4)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture
Client's address : P.O. Box 45, General Post Office, Hong Kong
Project : STF Environmental Team and Independent Environmental
Checker and EM&A Programme
Sample description : Twenty samples of stream water taken by the staff of Materialab
on 10/08/2012

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(4)/1 – WA121280(4)/20
Date of receipt of sample : 10/08/2012
Date test commenced : 11/08/2012
Date test completed : 13/08/2012
Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(4)


Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	42
2. C1 AE	41
3. C2 AE	4
4. C2 AE	4
5. W1 AE	7
6. W1 AE	8
7. W2 AE	15
8. W2 AE	15
9. W3 AE	5
10. W3 AE	5
11. C1 PF	7
12. C1 PF	8
13. C2 PF	6
14. C2 PF	5
15. W1 PF	31
16. W1 PF	29
17. W2 PF	31
18. W2 PF	33
19. W3 PF	17
20. W3 PF	16

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 16/8/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(4)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	30	29

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	98.4

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(5)



Page 1 of 2



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 13/08/2012

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(5)/1 – WA121280(5)/20

Date of receipt of sample : 13/08/2012

Date test commenced : 14/08/2012

Date test completed : 15/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(5)

Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	20
2. C1 AE	17
3. C2 AE	6
4. C2 AE	6
5. W1 AE	18
6. W1 AE	21
7. W2 AE	16
8. W2 AE	13
9. W3 AE	9
10. W3 AE	10
11. C1 PF	6
12. C1 PF	5
13. C2 PF	7
14. C2 PF	7
15. W1 PF	27
16. W1 PF	30
17. W2 PF	21
18. W2 PF	20
19. W3 PF	18
20. W3 PF	19

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 17/8/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(5)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 AE	20	22

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	97.8

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Report No. : 100440WA121280(6)



Page 1 of 2



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 15/08/2012

Client sample ID :

1. C1 AE	11. C1 PF
2. C1 AE	12. C1 PF
3. C2 AE	13. C2 PF
4. C2 AE	14. C2 PF
5. W1 AE	15. W1 PF
6. W1 AE	16. W1 PF
7. W2 AE	17. W2 PF
8. W2 AE	18. W2 PF
9. W3 AE	19. W3 PF
10. W3 AE	20. W3 PF

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(6)/1 – WA121280(6)/20

Date of receipt of sample : 15/08/2012

Date test commenced : 16/08/2012

Date test completed : 17/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(6)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AE	9
2. C1 AE	12
3. C2 AE	5
4. C2 AE	15
5. W1 AE	4
6. W1 AE	3
7. W2 AE	12
8. W2 AE	12
9. W3 AE	4
10. W3 AE	4
11. C1 PF	4
12. C1 PF	3
13. C2 PF	4
14. C2 PF	3
15. W1 PF	32
16. W1 PF	31
17. W2 PF	15
18. W2 PF	14
19. W3 PF	17
20. W3 PF	15

Supervised by : Y. M. ChungCertified by : Approved Signatory : HO Kin Man, John
Manager – Chemistry DepartmentDate : 21/8/2012****End of Report*****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(6)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 PF	30	31

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102.2

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(7)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 17/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(7)/1 – WA121280(7)/20

Date of receipt of sample : 17/08/2012

Date test commenced : 18/08/2012

Date test completed : 20/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab


Report No. : 100440WA121280(7)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	21
2. C1 AF	19
3. C2 AF	4
4. C2 AF	5
5. W1 AF	5
6. W1 AF	5
7. W2 AF	10
8. W2 AF	10
9. W3 AF	8
10. W3 AF	9
11. C1 PE	20
12. C1 PE	20
13. C2 PE	4
14. C2 PE	5
15. W1 PE	5
16. W1 PE	5
17. W2 PE	16
18. W2 PE	15
19. W3 PE	5
20. W3 PE	8

Supervised by : Y. M. Chung

Certified by : 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 27/8/2020****End of Report*****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Report No. : 100440WA121280(7)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 PE	15	16

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	101.6

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(8)



Page 1 of 2



TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of Materialab on 20/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(8)/1 – WA121280(8)/20

Date of receipt of sample : 20/08/2012

Date test commenced : 21/08/2012

Date test completed : 22/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(8)


Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	17
2. C1 AF	16
3. C2 AF	7
4. C2 AF	7
5. W1 AF	10
6. W1 AF	10
7. W2 AF	15
8. W2 AF	16
9. W3 AF	13
10. W3 AF	15
11. C1 PE	14
12. C1 PE	15
13. C2 PE	4
14. C2 PE	4
15. W1 PE	10
16. W1 PE	10
17. W2 PE	11
18. W2 PE	12
19. W3 PE	5
20. W3 PE	6

Supervised by : Y. M. Chung

Certified by 
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 27/8/2012

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(8)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 PE	12	13

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102.6

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Report No. : 100440WA121280(9)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of MaterialLab on 22/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(9)/1 – WA121280(9)/20

Date of receipt of sample : 22/08/2012

Date test commenced : 23/08/2012

Date test completed : 23/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


MaterialLab

Report No. : 100440WA121280(9)

Page 2 of 2

**Results:**

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	1900
2. C1 AF	1800
3. C2 AF	140
4. C2 AF	120
5. W1 AF	56
6. W1 AF	49
7. W2 AF	100
8. W2 AF	110
9. W3 AF	90
10. W3 AF	89
11. C1 PE	43
12. C1 PE	40
13. C2 PE	12
14. C2 PE	12
15. W1 PE	28
16. W1 PE	25
17. W2 PE	16
18. W2 PE	17
19. W3 PE	11
20. W3 PE	11

Supervised by : Y. M. Chung
 Certified by : 
 Approved Signatory : HO Kin Man, John
 Manager – Chemistry Department
Date : 7/9/2012****End of Report*****Note : This report refers only to the sample(s) tested.*

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(9)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W1 AF	51	48

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	99.8

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(10)



Page 1 of 2

TEST REPORT ON ANALYSIS OF WATER

Information Supplied by Client

Client : Veolia Water-Leighton-John Holland Joint Venture

Client's address : P.O. Box 45, General Post Office, Hong Kong

Project : STF Environmental Team and Independent Environmental Checker and EM&A Programme

Sample description : Twenty samples of stream water taken by the staff of Materialab on 24/08/2012

Client sample ID :

1. C1 AF	11. C1 PE
2. C1 AF	12. C1 PE
3. C2 AF	13. C2 PE
4. C2 AF	14. C2 PE
5. W1 AF	15. W1 PE
6. W1 AF	16. W1 PE
7. W2 AF	17. W2 PE
8. W2 AF	18. W2 PE
9. W3 AF	19. W3 PE
10. W3 AF	20. W3 PE

Test required : Total suspended solids dried at 103°C – 105°C

Laboratory Information

Lab. sample ID : WA121280(10)/1 – WA121280(10)/20

Date of receipt of sample : 24/08/2012

Date test commenced : 27/08/2012

Date test completed : 28/08/2012

Test method used : Total suspended solids dried at 103°C – 105°C
APHA 17ed. 2540D

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(10)

Page 2 of 2



Results:

Sample identification	Test parameters
	Total suspended solids dried at 103°C - 105°C, mg/L
1. C1 AF	10
2. C1 AF	11
3. C2 AF	3
4. C2 AF	2
5. W1 AF	15
6. W1 AF	13
7. W2 AF	38
8. W2 AF	28
9. W3 AF	16
10. W3 AF	15
11. C1 PE	21
12. C1 PE	24
13. C2 PE	4
14. C2 PE	3
15. W1 PE	9
16. W1 PE	11
17. W2 PE	18
18. W2 PE	14
19. W3 PE	6
20. W3 PE	5

Supervised by : Y. M. Chung

Certified by : *P. P. John*
Approved Signatory : HO Kin Man, John
Manager – Chemistry Department

Date : 31/8/12

****End of Report****

Note : This report refers only to the sample(s) tested.

The Hong Kong Accreditation Service (HKAS) has accredited Fugro Technical Services Limited under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this report were determined by this laboratory in accordance with its terms of accreditation. The copyright of this report is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the issuing laboratory.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Report No. : 100440WA121280(10)

Laboratory Duplicate Result

Sample ID	Original Result, mg/L	Duplicate Result, mg/L
W2 AF	30	26

Laboratory Blank

Sample ID	Result, mg/L	Detection Limit, mg/L
Pro Blank	<1	1

Laboratory QC sample

Sample ID	Assigned value, mg/L	Recovery, %
QC	50	102.4

Note : This report refers only to the sample(s) tested.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 25/07/2012 (p.m.) Test No. : 174
Tide State : MID-EBB Weather : RAINY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:51	25	5.5	S	1.0	27.2	< 0.5	< 1	25	
						27.3	< 0.5	< 1	24	
				B	4.5	27.2	< 0.5	< 1	21	
						27.2	< 0.5	< 1	22	
M2	16:38	25	4.0	S	1.0	27.2	< 0.5	< 1	< 20	
						27.2	< 0.5	< 1	< 20	
				B	3.0	27.1	< 0.5	< 1	< 20	
						27.1	< 0.5	< 1	< 20	
DM4	16:15	25	5.0	S	1.0	27.0	< 0.5	< 1	< 20	
						27.0	< 0.5	< 1	< 20	
				B	4.0	27.0	< 0.5	< 1	< 20	
						27.0	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 27/07/2012 (a.m.) Test No. : 175
Tide State : MID-EBB Weather : RAINY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	7:33	25	5.2	S	1.0	26.8	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
				B	4.2	26.7	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
M2	7:48	25	3.8	S	1.0	26.6	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
				B	2.8	26.7	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
DM4	8:13	25	4.4	S	1.0	26.7	< 0.5	< 1	< 20	
						26.7	< 0.5	< 1	< 20	
				B	3.4	26.7	< 0.5	< 1	< 20	
						26.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 27/07/2012 (p.m.) Test No. : 175
Tide State : MID-FLOOD Weather : RAINY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	13:17	25	4.9	S	1.0	27.1	< 0.5	< 1	< 20	
						27.2	< 0.5	< 1	< 20	
				B	3.9	26.7	< 0.5	< 1	< 20	
						26.8	< 0.5	< 1	< 20	
M2	13:30	25	3.7	S	1.0	27.6	< 0.5	< 1	< 20	
						27.6	< 0.5	< 1	< 20	
				B	2.7	27.8	< 0.5	< 1	< 20	
						27.8	< 0.5	< 1	< 20	
DM4	13:55	25	4.5	S	1.0	27.6	< 0.5	< 1	< 20	
						27.6	< 0.5	< 1	< 20	
				B	3.5	27.1	< 0.5	< 1	< 20	
						27.1	< 0.5	< 1	< 20	

Certified by :



Date :

11/9/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 30/07/2012 (a.m.) Test No. : 176
Tide State : MID-EBB Weather : SUNNY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	11:19	30	5.6	S	1.0	28.4	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	
				B	4.6	27.8	< 0.5	< 1	< 20	
						27.8	< 0.5	< 1	< 20	
M2	11:33	31	3.7	S	1.0	28.2	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
				B	2.7	27.9	< 0.5	< 1	< 20	
						27.9	< 0.5	< 1	< 20	
DM4	11:54	31	4.8	S	1.0	28.5	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	
				B	3.8	28.0	< 0.5	< 1	< 20	
						27.9	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN


Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 30/07/2012 (p.m.) Test No. : 176
Tide State : MID-FLOOD Weather : FINE
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	17:50	31	5.4	S	1.0	30.2	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	4.4	30.2	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
M2	18:04	31	3.5	S	1.0	29.3	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
				B	2.5	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
DM4	18:30	30	5.0	S	1.0	28.9	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
				B	4.0	28.3	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	

Certified by :  Date : 11/9/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk


Materialab

Our Ref. No. : 100440EN
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 01/08/2012 (a.m.) Test No. : 177
Tide State : MID-FLOOD Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	7:04	28	5.9	S	1.0	28.5	< 0.5	< 1	< 20	
						28.5	< 0.5	< 1	< 20	
				B	4.9	28.2	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
M2	7:18	28	4.6	S	1.0	28.5	< 0.5	< 1	< 20	
						28.5	< 0.5	< 1	< 20	
				B	3.6	27.7	< 0.5	< 1	< 20	
						27.7	< 0.5	< 1	< 20	
DM4	7:38	28	5.7	S	1.0	28.3	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	
				B	4.7	27.8	< 0.5	< 1	< 20	
						27.8	< 0.5	< 1	< 20	

Certified by :  Date : 11/9/2012
Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 01/08/2012 (p.m.) Test No. : 177
Tide State : MID-EBB Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	12:38	32	5.6	S	1.0	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	4.6	28.2	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
M2	12:51	32	3.8	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	2.8	28.2	< 0.5	< 1	< 20	
						28.2	< 0.5	< 1	< 20	
DM4	13:14	32	5.1	S	1.0	29.7	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	4.1	27.9	< 0.5	< 1	< 20	
						27.9	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 03/08/2012 (a.m.) Test No. : 178
Tide State : MID-FLOOD Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	8:15	30	5.8	S	1.0	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
				B	4.8	29.1	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
M2	8:27	30	4.7	S	1.0	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
				B	3.7	28.4	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	
DM4	8:49	30	5.7	S	1.0	29.2	< 0.5	< 1	< 20	
						29.1	< 0.5	< 1	< 20	
				B	4.7	28.3	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab


Our Ref. No. : 100440EN
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 03/08/2012 (p.m.) Test No. : 178
Tide State : MID-EBB Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	14:26	33	5.3	S	1.0	29.9	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	4.3	28.8	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
M2	14:39	33	3.7	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	2.7	28.7	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	
DM4	14:59	33	4.9	S	1.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	3.9	28.6	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

MaterialLab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 06/08/2012 (a.m.) Test No. : 179
Tide State : MID-FLOOD Weather : CLOUDY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:04	30	5.6	S	1.0	29.3	< 0.5	< 1	< 20	
						29.3	< 0.5	< 1	< 20	
				B	4.6	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
M2	10:17	30	4.1	S	1.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	3.0	28.8	< 0.5	< 1	< 20	
						28.7	< 0.5	< 1	< 20	
DM4	10:40	30	5.2	S	1.0	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
				B	4.2	28.7	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 06/08/2012 (p.m.) Test No. : 179
Tide State : MID-EBB Weather : CLOUDY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:14	30	5.4	S	1.0	29.7	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	4.4	28.9	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
M2	16:00	30	4.1	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	3.1	28.9	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
DM4	15:38	30	5.1	S	1.0	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	4.1	28.9	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 08/08/2012 (a.m.) Test No. : 180
Tide State : MID-FLOOD Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	11:36	32	5.5	S	1.0	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	4.5	29.7	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
M2	11:51	32	4.0	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	3.0	29.8	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
DM4	12:10	32	5.3	S	1.0	29.6	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	4.3	29.0	< 0.5	< 1	< 20	
						28.9	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 08/08/2012 (p.m.) Test No. : 180
Tide State : MID-EBB Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	16:33	34	5.7	S	1.0	31.0	< 0.5	< 1	< 20	
						31.0	< 0.5	< 1	< 20	
				B	4.7	29.1	< 0.5	< 1	< 20	
						29.0	< 0.5	< 1	< 20	
M2	16:46	34	3.8	S	1.0	31.3	< 0.5	< 1	< 20	
						31.3	< 0.5	< 1	< 20	
				B	2.8	30.7	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	
DM4	17:08	34	5.1	S	1.0	31.1	< 0.5	< 1	< 20	
						31.1	< 0.5	< 1	< 20	
				B	4.1	29.7	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 10/08/2012 (a.m.) Test No. : 181
Tide State : MID-EBB Weather : SUNNY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	7:17	30	5.2	S	1.0	30.0	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	4.2	30.2	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
M2	7:29	30	4.1	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	3.1	29.7	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
DM4	7:53	30	4.6	S	1.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
				B	3.6	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 10/08/2012 (p.m.)

Test No. : 181


Tide State : MID-FLOOD

Weather : CLOUDY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	13:53	32	5.0	S	1.0	30.9	< 0.5	< 1	< 20	Filling Work
						30.9	< 0.5	< 1	< 20	
				B	4.0	30.2	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
M2	14:06	31	3.8	S	1.0	30.1	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	2.8	30.0	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
DM4	14:27	31	4.8	S	1.0	30.7	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	
				B	3.8	30.7	< 0.5	< 1	< 20	
						30.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 13/08/2012 (a.m.) Test No. : 182
Tide State : MID-EBB Weather : CLOUDY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	10:28	29	5.4	S	1.0	29.7	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	
				B	4.4	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
M2	10:41	29	3.5	S	1.0	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
				B	2.5	29.8	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	
DM4	11:03	29	4.6	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	3.6	29.9	< 0.5	< 1	< 20	
						29.8	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 13/08/2012 (p.m.)

Test No. : 182


Tide State : MID-FLOOD

Weather : CLOUDY

Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	17:36	29	5.0	S	1.0	30.4	< 0.5	< 1	< 20	
						30.4	< 0.5	< 1	< 20	
				B	4.0	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	
M2	17:50	29	3.4	S	1.0	29.8	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	2.4	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
DM4	18:11	29	4.4	S	1.0	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	3.4	29.5	< 0.5	< 1	< 20	
						29.5	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 15/08/2012 (a.m.) Test No. : 183
Tide State : MID-EBB Weather : SUNNY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	11:40	32	5.3	S	1.0	30.8	< 0.5	< 1	< 20	
						30.9	< 0.5	< 1	< 20	
				B	4.3	28.5	< 0.5	< 1	< 20	
						28.6	< 0.5	< 1	< 20	
M2	11:53	33	3.9	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	2.9	28.8	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
DM4	12:13	32	4.7	S	1.0	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
				B	3.7	28.2	< 0.5	< 1	< 20	
						28.3	< 0.5	< 1	< 20	

Certified by :



Date : 11/9/2012

Approved Signatory : K.M. Ho

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 15/08/2012 (p.m.) Test No. : 183
Tide State : MID-FLOOD Weather : HAZY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	18:10	32	5.0	S	1.0	32.1	< 0.5	< 1	< 20	
						32.1	< 0.5	< 1	< 20	
				B	4.0	30.1	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
M2	18:25	32	3.7	S	1.0	30.1	< 0.5	< 1	< 20	
						30.1	< 0.5	< 1	< 20	
				B	2.7	30.0	< 0.5	< 1	< 20	
						30.0	< 0.5	< 1	< 20	
DM4	18:47	32	4.6	S	1.0	29.9	< 0.5	< 1	< 20	
						29.9	< 0.5	< 1	< 20	
				B	3.6	29.8	< 0.5	< 1	< 20	
						29.7	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN


Client : VW-VES (HK) Ltd.

Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 20/08/2012 (a.m.) Test No. : 184
Tide State : MID-FLOOD Weather : SUNNY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	9:24	30	5.8	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	4.8	29.4	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
M2	9:37	30	4.5	S	1.0	29.6	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
				B	3.5	28.8	< 0.5	< 1	< 20	
						28.8	< 0.5	< 1	< 20	
DM4	9:59	30	5.5	S	1.0	29.2	< 0.5	< 1	< 20	
						29.2	< 0.5	< 1	< 20	
				B	4.5	28.9	< 0.5	< 1	< 20	
						28.9	< 0.5	< 1	< 20	

Certified by : 
Approved Signatory : K.M. Ho

Date : 11/9/2012

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk

Materialab

Our Ref. No. : 100440EN

Client : VW-VES (HK) Ltd.


Project : Contract No. EP/SP/58/08

Field Data Record (Marine Water) - Testing of Cd, Cr and Al

Date : 20/08/2012 (p.m.) Test No. : 184
Tide State : MID-EBB Weather : SUNNY
Sea Condition : NORMAL

Location	Time	Ambient Temp. °C	Depth of water m	Depth sampled m		Water Temp. °C	Heavy metal, µg/L			Remarks
							Cadmium Content	Chromium Content	Aluminium Content	
M1	15:14	33	5.3	S	1.0	31.2	< 0.5	< 1	< 20	
						31.2	< 0.5	< 1	< 20	
				B	4.3	29.4	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	
M2	15:26	33	3.5	S	1.0	30.5	< 0.5	< 1	< 20	
						30.6	< 0.5	< 1	< 20	
				B	2.5	29.4	< 0.5	< 1	< 20	
						29.6	< 0.5	< 1	< 20	
DM4	15:46	33	4.8	S	1.0	30.2	< 0.5	< 1	< 20	
						30.2	< 0.5	< 1	< 20	
				B	3.8	29.4	< 0.5	< 1	< 20	
						29.4	< 0.5	< 1	< 20	

Certified by :



Approved Signatory : K.M. Ho

Date :

11/9/2012

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 3
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1219782
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 25-JUL-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 06-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 12
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 12
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H028278				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1219782 supersedes any previous reports with this reference. The completion date of analysis is 01-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1219782 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			LOR Unit	0.5 µg/L	1 µg/L	20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID		EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered		
M1-S-E-1	[25-JUL-2012]	HK1219782-001		<0.5	<1	25		
M1-S-E-2	[25-JUL-2012]	HK1219782-002		<0.5	<1	24		
M1-B-E-1	[25-JUL-2012]	HK1219782-003		<0.5	<1	21		
M1-B-E-2	[25-JUL-2012]	HK1219782-004		<0.5	<1	22		
M2-S-E-1	[25-JUL-2012]	HK1219782-005		<0.5	<1	<20		
M2-S-E-2	[25-JUL-2012]	HK1219782-006		<0.5	<1	<20		
M2-B-E-1	[25-JUL-2012]	HK1219782-007		<0.5	<1	<20		
M2-B-E-2	[25-JUL-2012]	HK1219782-008		<0.5	<1	<20		
DM4-S-E-1	[25-JUL-2012]	HK1219782-009		<0.5	<1	<20		
DM4-S-E-2	[25-JUL-2012]	HK1219782-010		<0.5	<1	<20		
DM4-B-E-1	[25-JUL-2012]	HK1219782-011		<0.5	<1	<20		
DM4-B-E-2	[25-JUL-2012]	HK1219782-012		<0.5	<1	<20		



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2422975)								
HK1219782-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1219782-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2422976)								
HK1219782-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	24	24	0.0
HK1219782-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2422975)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	99.4	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	97.3	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2422976)											
EG020: Aluminium	7429-90-5	10	µg/L	<20	100 µg/L	93.4	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report							
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)		
					MS	MSD	Low	High	Value	Control Limit	
EG: Metals and Major Cations - Filtered (QCLot: 2422975)											
HK1219782-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	103	----	75	125	----	----	
		EG020: Chromium	7440-47-3	10 µg/L	104	----	75	125	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2422976)											
HK1219782-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	98.3	----	75	125	----	----	

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1219887
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 27-JUL-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 06-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H028279-H028280				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1219887 supersedes any previous reports with this reference. The completion date of analysis is 01-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1219887 :
Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

Client sample ID	Client sampling date / time	Laboratory sample ID	Compound	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			LOR Unit	0.5 µg/L	1 µg/L	20 µg/L		
				EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered		
M1-S-E-1	27-JUL-2012 07:33	HK1219887-001		<0.5	<1	<20		
M1-S-E-2	27-JUL-2012 07:33	HK1219887-002		<0.5	<1	<20		
M1-B-E-1	27-JUL-2012 07:33	HK1219887-003		<0.5	<1	<20		
M1-B-E-2	27-JUL-2012 07:33	HK1219887-004		<0.5	<1	<20		
M2-S-E-1	27-JUL-2012 07:48	HK1219887-005		<0.5	<1	<20		
M2-S-E-2	27-JUL-2012 07:48	HK1219887-006		<0.5	<1	<20		
M2-B-E-1	27-JUL-2012 07:48	HK1219887-007		<0.5	<1	<20		
M2-B-E-2	27-JUL-2012 07:48	HK1219887-008		<0.5	<1	<20		
DM4-S-E-1	27-JUL-2012 08:13	HK1219887-009		<0.5	<1	<20		
DM4-S-E-2	27-JUL-2012 08:13	HK1219887-010		<0.5	<1	<20		
DM4-B-E-1	27-JUL-2012 08:13	HK1219887-011		<0.5	<1	<20		
DM4-B-E-2	27-JUL-2012 08:13	HK1219887-012		<0.5	<1	<20		
M1-S-F-1	27-JUL-2012 13:17	HK1219887-013		<0.5	<1	<20		
M1-S-F-2	27-JUL-2012 13:17	HK1219887-014		<0.5	<1	<20		
M1-B-F-1	27-JUL-2012 13:17	HK1219887-015		<0.5	<1	<20		
M1-B-F-2	27-JUL-2012 13:17	HK1219887-016		<0.5	<1	<20		
M2-S-F-1	27-JUL-2012 13:30	HK1219887-017		<0.5	<1	<20		
M2-S-F-2	27-JUL-2012 13:30	HK1219887-018		<0.5	<1	<20		
M2-B-F-1	27-JUL-2012 13:30	HK1219887-019		<0.5	<1	<20		
M2-B-F-2	27-JUL-2012 13:30	HK1219887-020		<0.5	<1	<20		
DM4-S-F-1	27-JUL-2012 13:55	HK1219887-021		<0.5	<1	<20		
DM4-S-F-2	27-JUL-2012 13:55	HK1219887-022		<0.5	<1	<20		
DM4-B-F-1	27-JUL-2012 13:55	HK1219887-023		<0.5	<1	<20		
DM4-B-F-2	27-JUL-2012 13:55	HK1219887-024		<0.5	<1	<20		



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2425627)								
HK1219887-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1219887-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2425628)								
HK1219887-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1219887-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2425629)								
HK1219887-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2425630)								
HK1219887-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2425627)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	107	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	104	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2425628)											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	99.2	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2425629)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	107	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	112	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2425630)											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	104	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2425627)										
HK1219887-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	105	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	105	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2425628)										
HK1219887-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	94.2	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2425629)										
HK1219887-021	DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	112	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	104	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2425630)										
HK1219887-021	DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	107	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1220040
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 30-JUL-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 08-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014021, H028281				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1220040 supersedes any previous reports with this reference. The completion date of analysis is 01-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1220040 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

Client sample ID	Client sampling date / time	Laboratory sample ID	Compound LOR Unit	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			0.5 µg/L	1 µg/L	20 µg/L			
			EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	30-JUL-2012 11:19	HK1220040-001	<0.5	<1	<20			
M1-S-E-2	30-JUL-2012 11:19	HK1220040-002	<0.5	<1	<20			
M1-B-E-1	30-JUL-2012 11:19	HK1220040-003	<0.5	<1	<20			
M1-B-E-2	30-JUL-2012 11:19	HK1220040-004	<0.5	<1	<20			
M2-S-E-1	30-JUL-2012 11:33	HK1220040-005	<0.5	<1	<20			
M2-S-E-2	30-JUL-2012 11:33	HK1220040-006	<0.5	<1	<20			
M2-B-E-1	30-JUL-2012 11:33	HK1220040-007	<0.5	<1	<20			
M2-B-E-2	30-JUL-2012 11:33	HK1220040-008	<0.5	<1	<20			
DM4-S-E-1	30-JUL-2012 11:54	HK1220040-009	<0.5	<1	<20			
DM4-S-E-2	30-JUL-2012 11:54	HK1220040-010	<0.5	<1	<20			
DM4-B-E-1	30-JUL-2012 11:54	HK1220040-011	<0.5	<1	<20			
DM4-B-E-2	30-JUL-2012 11:54	HK1220040-012	<0.5	<1	<20			
M1-S-F-1	30-JUL-2012 17:50	HK1220040-013	<0.5	<1	<20			
M1-S-F-2	30-JUL-2012 17:50	HK1220040-014	<0.5	<1	<20			
M1-B-F-1	30-JUL-2012 17:50	HK1220040-015	<0.5	<1	<20			
M1-B-F-2	30-JUL-2012 17:50	HK1220040-016	<0.5	<1	<20			
M2-S-F-1	30-JUL-2012 18:04	HK1220040-017	<0.5	<1	<20			
M2-S-F-2	30-JUL-2012 18:04	HK1220040-018	<0.5	<1	<20			
M2-B-F-1	30-JUL-2012 18:04	HK1220040-019	<0.5	<1	<20			
M2-B-F-2	30-JUL-2012 18:04	HK1220040-020	<0.5	<1	<20			
DM4-S-F-1	30-JUL-2012 18:30	HK1220040-021	<0.5	<1	<20			
DM4-S-F-2	30-JUL-2012 18:30	HK1220040-022	<0.5	<1	<20			
DM4-B-F-1	30-JUL-2012 18:30	HK1220040-023	<0.5	<1	<20			
DM4-B-F-2	30-JUL-2012 18:30	HK1220040-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2429790)								
HK1220040-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220040-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2429791)								
HK1220040-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220040-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2429792)								
HK1220040-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2429793)								
HK1220040-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2429790)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	110	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	112	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2429791)											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	104	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2429792)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	107	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	108	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2429793)											
EG020: Aluminium	7429-90-5	10	µg/L	<20	10 µg/L	103	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2429790)										
HK1220040-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	104	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	103	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2429791)										
HK1220040-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	117	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
				Concentration	MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2429792)										
HK1220040-021	DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	107	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	97.2	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2429793)										
HK1220040-021	DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	98.6	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1220205
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 01-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 14-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014022, H014023				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1220205 supersedes any previous reports with this reference. The completion date of analysis is 07-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1220205 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics

ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	01-AUG-2012 07:04	HK1220205-001	<0.5	<1	<20			
M1-S-F-2	01-AUG-2012 07:04	HK1220205-002	<0.5	<1	<20			
M1-B-F-1	01-AUG-2012 07:04	HK1220205-003	<0.5	<1	<20			
M1-B-F-2	01-AUG-2012 07:04	HK1220205-004	<0.5	<1	<20			
M2-S-F-1	01-AUG-2012 07:18	HK1220205-005	<0.5	<1	<20			
M2-S-F-2	01-AUG-2012 07:18	HK1220205-006	<0.5	<1	<20			
M2-B-F-1	01-AUG-2012 07:18	HK1220205-007	<0.5	<1	<20			
M2-B-F-2	01-AUG-2012 07:18	HK1220205-008	<0.5	<1	<20			
DM4-S-F-1	01-AUG-2012 07:38	HK1220205-009	<0.5	<1	<20			
DM4-S-F-2	01-AUG-2012 07:38	HK1220205-010	<0.5	<1	<20			
DM4-B-F-1	01-AUG-2012 07:38	HK1220205-011	<0.5	<1	<20			
DM4-B-F-2	01-AUG-2012 07:38	HK1220205-012	<0.5	<1	<20			
M1-S-E-1	01-AUG-2012 12:38	HK1220205-013	<0.5	<1	<20			
M1-S-E-2	01-AUG-2012 12:38	HK1220205-014	<0.5	<1	<20			
M1-B-E-1	01-AUG-2012 12:38	HK1220205-015	<0.5	<1	<20			
M1-B-E-2	01-AUG-2012 12:38	HK1220205-016	<0.5	<1	<20			
M2-S-E-1	01-AUG-2012 12:51	HK1220205-017	<0.5	<1	<20			
M2-S-E-2	01-AUG-2012 12:51	HK1220205-018	<0.5	<1	<20			
M2-B-E-1	01-AUG-2012 12:51	HK1220205-019	<0.5	<1	<20			
M2-B-E-2	01-AUG-2012 12:51	HK1220205-020	<0.5	<1	<20			
DM4-S-E-1	01-AUG-2012 13:14	HK1220205-021	<0.5	<1	<20			
DM4-S-E-2	01-AUG-2012 13:14	HK1220205-022	<0.5	<1	<20			
DM4-B-E-1	01-AUG-2012 13:14	HK1220205-023	<0.5	<1	<20			
DM4-B-E-2	01-AUG-2012 13:14	HK1220205-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2437573)								
HK1220205-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220205-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2437574)								
HK1220205-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220205-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2437575)								
HK1220205-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2437576)								
HK1220205-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QC Lot: 2437573)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	93.6	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	106	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QC Lot: 2437574)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	93.6	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QC Lot: 2437575)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	101	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	105	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QC Lot: 2437576)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	104	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QC Lot: 2437573)										
HK1220205-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	94.2	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	96.3	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QC Lot: 2437574)										
HK1220205-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	77.9	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2437575)										
HK1220205-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	98.1	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	99.6	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2437576)										
HK1220205-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	98.1	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1220562
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 03-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 14-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014024-H014025				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1220562 supersedes any previous reports with this reference. The completion date of analysis is 11-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1220562 :
Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	03-AUG-2012 08:15	HK1220562-001	<0.5	<1	<20			
M1-S-F-2	03-AUG-2012 08:15	HK1220562-002	<0.5	<1	<20			
M1-B-F-1	03-AUG-2012 08:15	HK1220562-003	<0.5	<1	<20			
M1-B-F-2	03-AUG-2012 08:15	HK1220562-004	<0.5	<1	<20			
M2-S-F-1	03-AUG-2012 08:27	HK1220562-005	<0.5	<1	<20			
M2-S-F-2	03-AUG-2012 08:27	HK1220562-006	<0.5	<1	<20			
M2-B-F-1	03-AUG-2012 08:27	HK1220562-007	<0.5	<1	<20			
M2-B-F-2	03-AUG-2012 08:27	HK1220562-008	<0.5	<1	<20			
DM4-S-F-1	03-AUG-2012 08:49	HK1220562-009	<0.5	<1	<20			
DM4-S-F-2	03-AUG-2012 08:49	HK1220562-010	<0.5	<1	<20			
DM4-B-F-1	03-AUG-2012 08:49	HK1220562-011	<0.5	<1	<20			
DM4-B-F-2	03-AUG-2012 08:49	HK1220562-012	<0.5	<1	<20			
M1-S-E-1	03-AUG-2012 14:26	HK1220562-013	<0.5	<1	<20			
M1-S-E-2	03-AUG-2012 14:26	HK1220562-014	<0.5	<1	<20			
M1-B-E-1	03-AUG-2012 14:26	HK1220562-015	<0.5	<1	<20			
M1-B-E-2	03-AUG-2012 14:26	HK1220562-016	<0.5	<1	<20			
M2-S-E-1	03-AUG-2012 14:39	HK1220562-017	<0.5	<1	<20			
M2-S-E-2	03-AUG-2012 14:39	HK1220562-018	<0.5	<1	<20			
M2-B-E-1	03-AUG-2012 14:39	HK1220562-019	<0.5	<1	<20			
M2-B-E-2	03-AUG-2012 14:39	HK1220562-020	<0.5	<1	<20			
DM4-S-E-1	03-AUG-2012 14:59	HK1220562-021	<0.5	<1	<20			
DM4-S-E-2	03-AUG-2012 14:59	HK1220562-022	<0.5	<1	<20			
DM4-B-E-1	03-AUG-2012 14:59	HK1220562-023	<0.5	<1	<20			
DM4-B-E-2	03-AUG-2012 14:59	HK1220562-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2442483)								
HK1220562-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220562-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442484)								
HK1220562-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220562-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442485)								
HK1220562-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220716-007	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442486)								
HK1220562-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220716-007	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442483)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	90.6	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	100	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442484)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	98.3	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442485)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	91.2	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	93.3	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442486)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	111	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442483)										
HK1220562-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	99.6	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	79.5	----	75	125	----	----



Matrix: WATER

					Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report					
				Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number		MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442484)										
HK1220562-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	107	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442485)										
HK1220562-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	97.1	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	93.8	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442486)										
HK1220562-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	76.8	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1220716
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 06-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 15-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014026-H014027				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1220716 supersedes any previous reports with this reference. The completion date of analysis is 11-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1220716 :
Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

Client sample ID	Client sampling date / time	Laboratory sample ID	Compound	EG020: Cadmium	EG020: Chromium	EG020: Aluminium		
			LOR Unit	0.5 µg/L	1 µg/L	20 µg/L		
				EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered		
M1-S-F-1	06-AUG-2012 10:04	HK1220716-001		<0.5	<1	<20		
M1-S-F-2	06-AUG-2012 10:04	HK1220716-002		<0.5	<1	<20		
M1-B-F-1	06-AUG-2012 10:04	HK1220716-003		<0.5	<1	<20		
M1-B-F-2	06-AUG-2012 10:04	HK1220716-004		<0.5	<1	<20		
M2-S-F-1	06-AUG-2012 10:17	HK1220716-005		<0.5	<1	<20		
M2-S-F-2	06-AUG-2012 10:17	HK1220716-006		<0.5	<1	<20		
M2-B-F-1	06-AUG-2012 10:17	HK1220716-007		<0.5	<1	<20		
M2-B-F-2	06-AUG-2012 10:17	HK1220716-008		<0.5	<1	<20		
DM4-S-F-1	06-AUG-2012 10:40	HK1220716-009		<0.5	<1	<20		
DM4-S-F-2	06-AUG-2012 10:40	HK1220716-010		<0.5	<1	<20		
DM4-B-F-1	06-AUG-2012 10:40	HK1220716-011		<0.5	<1	<20		
DM4-B-F-2	06-AUG-2012 10:40	HK1220716-012		<0.5	<1	<20		
M1-S-E-1	06-AUG-2012 16:14	HK1220716-013		<0.5	<1	<20		
M1-S-E-2	06-AUG-2012 16:14	HK1220716-014		<0.5	<1	<20		
M1-B-E-1	06-AUG-2012 16:14	HK1220716-015		<0.5	<1	<20		
M1-B-E-2	06-AUG-2012 16:14	HK1220716-016		<0.5	<1	<20		
M2-S-E-1	06-AUG-2012 16:00	HK1220716-017		<0.5	<1	<20		
M2-S-E-2	06-AUG-2012 16:00	HK1220716-018		<0.5	<1	<20		
M2-B-E-1	06-AUG-2012 16:00	HK1220716-019		<0.5	<1	<20		
M2-B-E-2	06-AUG-2012 16:00	HK1220716-020		<0.5	<1	<20		
DM4-S-E-1	06-AUG-2012 15:38	HK1220716-021		<0.5	<1	<20		
DM4-S-E-2	06-AUG-2012 15:38	HK1220716-022		<0.5	<1	<20		
DM4-B-E-1	06-AUG-2012 15:38	HK1220716-023		<0.5	<1	<20		
DM4-B-E-2	06-AUG-2012 15:38	HK1220716-024		<0.5	<1	<20		



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2442485)								
HK1220562-022	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220716-007	M2-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442486)								
HK1220562-022	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220716-007	M2-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442487)								
HK1220716-018	M2-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2442488)								
HK1220716-018	M2-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442485)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	91.2	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	93.3	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442486)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	111	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442487)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	94.6	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	101	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442488)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	92.6	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442485)										
HK1220562-021	Anonymous	EG020: Cadmium	7440-43-9	10 µg/L	97.1	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	93.8	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442486)										
HK1220562-021	Anonymous	EG020: Aluminium	7429-90-5	10 µg/L	76.8	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2442487)										
HK1220716-017	M2-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	84.9	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2442488)										
HK1220716-017	M2-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	78.6	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1220982
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 08-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 17-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014028-H014029				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1220982 supersedes any previous reports with this reference. The completion date of analysis is 16-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1220982 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	08-AUG-2012 11:36	HK1220982-001	<0.5	<1	<20			
M1-S-F-2	08-AUG-2012 11:36	HK1220982-002	<0.5	<1	<20			
M1-B-F-1	08-AUG-2012 11:36	HK1220982-003	<0.5	<1	<20			
M1-B-F-2	08-AUG-2012 11:36	HK1220982-004	<0.5	<1	<20			
M2-S-F-1	08-AUG-2012 11:51	HK1220982-005	<0.5	<1	<20			
M2-S-F-2	08-AUG-2012 11:51	HK1220982-006	<0.5	<1	<20			
M2-B-F-1	08-AUG-2012 11:51	HK1220982-007	<0.5	<1	<20			
M2-B-F-2	08-AUG-2012 11:51	HK1220982-008	<0.5	<1	<20			
DM4-S-F-1	08-AUG-2012 12:10	HK1220982-009	<0.5	<1	<20			
DM4-S-F-2	08-AUG-2012 12:10	HK1220982-010	<0.5	<1	<20			
DM4-B-F-1	08-AUG-2012 12:10	HK1220982-011	<0.5	<1	<20			
DM4-B-F-2	08-AUG-2012 12:10	HK1220982-012	<0.5	<1	<20			
M1-S-E-1	08-AUG-2012 16:33	HK1220982-013	<0.5	<1	<20			
M1-S-E-2	08-AUG-2012 16:33	HK1220982-014	<0.5	<1	<20			
M1-B-E-1	08-AUG-2012 16:33	HK1220982-015	<0.5	<1	<20			
M1-B-E-2	08-AUG-2012 16:33	HK1220982-016	<0.5	<1	<20			
M2-S-E-1	08-AUG-2012 16:46	HK1220982-017	<0.5	<1	<20			
M2-S-E-2	08-AUG-2012 16:46	HK1220982-018	<0.5	<1	<20			
M2-B-E-1	08-AUG-2012 16:46	HK1220982-019	<0.5	<1	<20			
M2-B-E-2	08-AUG-2012 16:46	HK1220982-020	<0.5	<1	<20			
DM4-S-E-1	08-AUG-2012 17:08	HK1220982-021	<0.5	<1	<20			
DM4-S-E-2	08-AUG-2012 17:08	HK1220982-022	<0.5	<1	<20			
DM4-B-E-1	08-AUG-2012 17:08	HK1220982-023	<0.5	<1	<20			
DM4-B-E-2	08-AUG-2012 17:08	HK1220982-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2451819)								
HK1220982-002	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1220982-011	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451820)								
HK1220982-002	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1220982-011	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451821)								
HK1220982-022	DM4-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221264-007	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451822)								
HK1220982-022	DM4-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221264-007	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)		
						LCS	DCS	Low	High	Value	Control Limit	
EG: Metals and Major Cations - Filtered (QCLot: 2451819)												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	91.7	----	80	112	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	91.7	----	80	114	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2451820)												
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	93.7	----	85	115	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2451821)												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	94.0	----	80	112	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	96.1	----	80	114	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2451822)												
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	107	----	85	115	----	----	

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451819)										
HK1220982-001	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	90.8	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	86.2	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451820)										
HK1220982-001	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	84.2	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451821)										
HK1220982-021	DM4-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	92.3	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	89.3	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451822)										
HK1220982-021	DM4-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	88.2	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1221264
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 10-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 21-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014030-H014031				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1221264 supersedes any previous reports with this reference. The completion date of analysis is 16-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1221264 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	10-AUG-2012 07:17	HK1221264-001	<0.5	<1	<20			
M1-S-E-2	10-AUG-2012 07:17	HK1221264-002	<0.5	<1	<20			
M1-B-E-1	10-AUG-2012 07:17	HK1221264-003	<0.5	<1	<20			
M1-B-E-2	10-AUG-2012 07:17	HK1221264-004	<0.5	<1	<20			
M2-S-E-1	10-AUG-2012 07:29	HK1221264-005	<0.5	<1	<20			
M2-S-E-2	10-AUG-2012 07:29	HK1221264-006	<0.5	<1	<20			
M2-B-E-1	10-AUG-2012 07:29	HK1221264-007	<0.5	<1	<20			
M2-B-E-2	10-AUG-2012 07:29	HK1221264-008	<0.5	<1	<20			
DM4-S-E-1	10-AUG-2012 07:53	HK1221264-009	<0.5	<1	<20			
DM4-S-E-2	10-AUG-2012 07:53	HK1221264-010	<0.5	<1	<20			
DM4-B-E-1	10-AUG-2012 07:53	HK1221264-011	<0.5	<1	<20			
DM4-B-E-2	10-AUG-2012 07:53	HK1221264-012	<0.5	<1	<20			
M1-S-F-1	10-AUG-2012 13:52	HK1221264-013	<0.5	<1	<20			
M1-S-F-2	10-AUG-2012 13:52	HK1221264-014	<0.5	<1	<20			
M1-B-F-1	10-AUG-2012 13:52	HK1221264-015	<0.5	<1	<20			
M1-B-F-2	10-AUG-2012 13:52	HK1221264-016	<0.5	<1	<20			
M2-S-F-1	10-AUG-2012 14:06	HK1221264-017	<0.5	<1	<20			
M2-S-F-2	10-AUG-2012 14:06	HK1221264-018	<0.5	<1	<20			
M2-B-F-1	10-AUG-2012 14:06	HK1221264-019	<0.5	<1	<20			
M2-B-F-2	10-AUG-2012 14:06	HK1221264-020	<0.5	<1	<20			
DM4-S-F-1	10-AUG-2012 14:27	HK1221264-021	<0.5	<1	<20			
DM4-S-F-2	10-AUG-2012 14:27	HK1221264-022	<0.5	<1	<20			
DM4-B-F-1	10-AUG-2012 14:27	HK1221264-023	<0.5	<1	<20			
DM4-B-F-2	10-AUG-2012 14:27	HK1221264-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2451821)								
HK1220982-022	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221264-007	M2-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451822)								
HK1220982-022	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221264-007	M2-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451823)								
HK1221264-018	M2-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221380-003	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451824)								
HK1221380-003	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221380-014	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451821)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	94.0	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	96.1	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451822)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	107	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451823)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	99.9	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	98.5	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451824)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	100	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451821)										
HK1220982-021	Anonymous	EG020: Cadmium	7440-43-9	10 µg/L	92.3	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	89.3	----	75	125	----	----



Matrix: WATER

					Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report					
				Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number		MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451822)										
HK1220982-021	Anonymous	EG020: Aluminium	7429-90-5	10 µg/L	88.2	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451823)										
HK1221264-017	M2-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	95.7	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451824)										
HK1221264-017	M2-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	100	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1221380
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 13-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 22-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014032-H014033				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1221380 supersedes any previous reports with this reference. The completion date of analysis is 16-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1221380 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	13-AUG-2012 10:28	HK1221380-001	<0.5	<1	<20			
M1-S-E-2	13-AUG-2012 10:28	HK1221380-002	<0.5	<1	<20			
M1-B-E-1	13-AUG-2012 10:28	HK1221380-003	<0.5	<1	<20			
M1-B-E-2	13-AUG-2012 10:28	HK1221380-004	<0.5	<1	<20			
M2-S-E-1	13-AUG-2012 10:41	HK1221380-005	<0.5	<1	<20			
M2-S-E-2	13-AUG-2012 10:41	HK1221380-006	<0.5	<1	<20			
M2-B-E-1	13-AUG-2012 10:41	HK1221380-007	<0.5	<1	<20			
M2-B-E-2	13-AUG-2012 10:41	HK1221380-008	<0.5	<1	<20			
DM4-S-E-1	13-AUG-2012 11:03	HK1221380-009	<0.5	<1	<20			
DM4-S-E-2	13-AUG-2012 11:03	HK1221380-010	<0.5	<1	<20			
DM4-B-E-1	13-AUG-2012 11:03	HK1221380-011	<0.5	<1	<20			
DM4-B-E-2	13-AUG-2012 11:03	HK1221380-012	<0.5	<1	<20			
M1-S-F-1	13-AUG-2012 17:36	HK1221380-013	<0.5	<1	<20			
M1-S-F-2	13-AUG-2012 17:36	HK1221380-014	<0.5	<1	<20			
M1-B-F-1	13-AUG-2012 17:36	HK1221380-015	<0.5	<1	<20			
M1-B-F-2	13-AUG-2012 17:36	HK1221380-016	<0.5	<1	<20			
M2-S-F-1	13-AUG-2012 17:50	HK1221380-017	<0.5	<1	<20			
M2-S-F-2	13-AUG-2012 17:50	HK1221380-018	<0.5	<1	<20			
M2-B-F-1	13-AUG-2012 17:50	HK1221380-019	<0.5	<1	<20			
M2-B-F-2	13-AUG-2012 17:50	HK1221380-020	<0.5	<1	<20			
DM4-S-F-1	13-AUG-2012 18:11	HK1221380-021	<0.5	<1	<20			
DM4-S-F-2	13-AUG-2012 18:11	HK1221380-022	<0.5	<1	<20			
DM4-B-F-1	13-AUG-2012 18:11	HK1221380-023	<0.5	<1	<20			
DM4-B-F-2	13-AUG-2012 18:11	HK1221380-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2451823)								
HK1221264-018	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221380-003	M1-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451824)								
HK1221380-003	M1-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221380-014	M1-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451827)								
HK1221380-014	M1-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221380-023	DM4-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2451828)								
HK1221264-018	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221380-023	DM4-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451823)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	99.9	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	98.5	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451824)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	100	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451827)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	92.0	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	95.2	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451828)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	103	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451823)										
HK1221264-017	Anonymous	EG020: Cadmium	7440-43-9	10 µg/L	101	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	95.7	----	75	125	----	----



Matrix: WATER

					Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report					
				Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number		MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2451824)										
HK1221264-017	Anonymous	EG020: Aluminium	7429-90-5	10 µg/L	100	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451827)										
HK1221380-013	M1-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	90.2	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	83.8	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2451828)										
HK1221380-013	M1-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	104	----	75	125	----	----

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1221672
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 15-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 24-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014034-H014035				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1221672 supersedes any previous reports with this reference. The completion date of analysis is 23-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1221672 :

- Sample(s) were received in a chilled condition.
- Water sample(s) analysed and reported on an as received basis.
- Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-E-1	15-AUG-2012 11:40	HK1221672-001	<0.5	<1	<20			
M1-S-E-2	15-AUG-2012 11:40	HK1221672-002	<0.5	<1	<20			
M1-B-E-1	15-AUG-2012 11:40	HK1221672-003	<0.5	<1	<20			
M1-B-E-2	15-AUG-2012 11:40	HK1221672-004	<0.5	<1	<20			
M2-S-E-1	15-AUG-2012 11:53	HK1221672-005	<0.5	<1	<20			
M2-S-E-2	15-AUG-2012 11:53	HK1221672-006	<0.5	<1	<20			
M2-B-E-1	15-AUG-2012 11:53	HK1221672-007	<0.5	<1	<20			
M2-B-E-2	15-AUG-2012 11:53	HK1221672-008	<0.5	<1	<20			
DM4-S-E-1	15-AUG-2012 12:13	HK1221672-009	<0.5	<1	<20			
DM4-S-E-2	15-AUG-2012 12:13	HK1221672-010	<0.5	<1	<20			
DM4-B-E-1	15-AUG-2012 12:13	HK1221672-011	<0.5	<1	<20			
DM4-B-E-2	15-AUG-2012 12:13	HK1221672-012	<0.5	<1	<20			
M1-S-F-1	15-AUG-2012 18:10	HK1221672-013	<0.5	<1	<20			
M1-S-F-2	15-AUG-2012 18:10	HK1221672-014	<0.5	<1	<20			
M1-B-F-1	15-AUG-2012 18:10	HK1221672-015	<0.5	<1	<20			
M1-B-F-2	15-AUG-2012 18:10	HK1221672-016	<0.5	<1	<20			
M2-S-F-1	15-AUG-2012 18:25	HK1221672-017	<0.5	<1	<20			
M2-S-F-2	15-AUG-2012 18:25	HK1221672-018	<0.5	<1	<20			
M2-B-F-1	15-AUG-2012 18:25	HK1221672-019	<0.5	<1	<20			
M2-B-F-2	15-AUG-2012 18:25	HK1221672-020	<0.5	<1	<20			
DM4-S-F-1	15-AUG-2012 18:47	HK1221672-021	<0.5	<1	<20			
DM4-S-F-2	15-AUG-2012 18:47	HK1221672-022	<0.5	<1	<20			
DM4-B-F-1	15-AUG-2012 18:47	HK1221672-023	<0.5	<1	<20			
DM4-B-F-2	15-AUG-2012 18:47	HK1221672-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2463250)								
HK1221672-002	M1-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1221672-011	DM4-B-E-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463251)								
HK1221672-002	M1-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1221672-011	DM4-B-E-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463252)								
HK1221672-022	DM4-S-F-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1222046-007	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463253)								
HK1221672-022	DM4-S-F-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1222046-007	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)		
						LCS	DCS	Low	High	Value	Control Limit	
EG: Metals and Major Cations - Filtered (QCLot: 2463250)												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	95.3	----	80	112	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	94.9	----	80	114	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2463251)												
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	101	----	85	115	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2463252)												
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	93.4	----	80	112	----	----	
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	92.0	----	80	114	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2463253)												
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	106	----	85	115	----	----	

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2463250)										
HK1221672-001	M1-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	110	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	103	----	75	125	----	----



Matrix: WATER

Laboratory sample ID					Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
					Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2463251)											
HK1221672-001	M1-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	97.5	----	75	125	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2463252)											
HK1221672-021	DM4-S-F-1	EG020: Cadmium	7440-43-9	10 µg/L	106	----	75	125	----	----	
		EG020: Chromium	7440-47-3	10 µg/L	98.7	----	75	125	----	----	
EG: Metals and Major Cations - Filtered (QCLot: 2463253)											
HK1221672-021	DM4-S-F-1	EG020: Aluminium	7429-90-5	10 µg/L	102	----	75	125	----	----	

CERTIFICATE OF ANALYSIS

<i>Client</i>	: FUGRO TECHNICAL SERVICES LIMITED	<i>Laboratory</i>	: ALS Technichem HK Pty Ltd	<i>Page</i>	: 1 of 4
<i>Contact</i>	: MR JOHN K.M. HO	<i>Contact</i>	: Chan Kwok Fai, Godfrey	<i>Work Order</i>	: HK1222046
<i>Address</i>	: MATERIAL DIVISION FUGRO DEVELOPMENT CENTRE, NO 5 LOK YI STREET, 17 M.S. CASTLE PEAK ROAD, TAI LAM, TUEN MUN, N.T. HONG KONG	<i>Address</i>	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
<i>E-mail</i>	: jho@fugro.com.hk	<i>E-mail</i>	: Godfrey.Chan@alsglobal.com	<i>Date received</i>	: 20-AUG-2012
<i>Telephone</i>	: +852 2452 7142	<i>Telephone</i>	: +852 2610 1044	<i>Date of issue</i>	: 29-AUG-2012
<i>Facsimile</i>	: +852 2450 6138	<i>Facsimile</i>	: +852 2610 2021	<i>No. of samples</i>	- Received : 24
<i>Project</i>	: ----	<i>Quote number</i>	: ----		- Analysed : 24
<i>Order number</i>	: ----				
<i>C-O-C number</i>	: H014036-H014037				
<i>Site</i>	: ----				

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1222046 supersedes any previous reports with this reference. The completion date of analysis is 23-AUG-2012. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1222046 :
Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.
Water sample(s) were filtered prior to dissolved metal analysis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd. Hong Kong Accreditation Service (HKAS) has accredited this laboratory (ALS Technichem (HK) Pty Ltd) under Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific laboratory activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

<i>Signatory</i>	<i>Position</i>	<i>Authorised results for:-</i>
Kwok Ka Yan, Yankee	Chemist - Metals	Inorganics
Wong Wing, Kenneth	Assistant Supervisor - Metals	Inorganics

ALS Laboratory Group

Trading Name: **ALS Technichem (HK) Pty Ltd**

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, N.T., Hong Kong
Tel: +852 2610 1044 Fax: +852 2610 2021 www.alsenviro.com

A Campbell Brothers Limited Company



Analytical Results

Sub-Matrix: SEAWATER

			Compound LOR Unit	EG020: Cadmium 0.5 µg/L	EG020: Chromium 1 µg/L	EG020: Aluminium 20 µg/L		
Client sample ID	Client sampling date / time	Laboratory sample ID	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered	EG: Metals and Major Cations - Filtered			
M1-S-F-1	20-AUG-2012 09:24	HK1222046-001	<0.5	<1	<20			
M1-S-F-2	20-AUG-2012 09:24	HK1222046-002	<0.5	<1	<20			
M1-B-F-1	20-AUG-2012 09:24	HK1222046-003	<0.5	<1	<20			
M1-B-F-2	20-AUG-2012 09:24	HK1222046-004	<0.5	<1	<20			
M2-S-F-1	20-AUG-2012 09:37	HK1222046-005	<0.5	<1	<20			
M2-S-F-2	20-AUG-2012 09:37	HK1222046-006	<0.5	<1	<20			
M2-B-F-1	20-AUG-2012 09:37	HK1222046-007	<0.5	<1	<20			
M2-B-F-2	20-AUG-2012 09:37	HK1222046-008	<0.5	<1	<20			
DM4-S-F-1	20-AUG-2012 09:59	HK1222046-009	<0.5	<1	<20			
DM4-S-F-2	20-AUG-2012 09:59	HK1222046-010	<0.5	<1	<20			
DM4-B-F-1	20-AUG-2012 09:59	HK1222046-011	<0.5	<1	<20			
DM4-B-F-2	20-AUG-2012 09:59	HK1222046-012	<0.5	<1	<20			
M1-S-E-1	20-AUG-2012 15:14	HK1222046-013	<0.5	<1	<20			
M1-S-E-2	20-AUG-2012 15:14	HK1222046-014	<0.5	<1	<20			
M1-B-E-1	20-AUG-2012 15:14	HK1222046-015	<0.5	<1	<20			
M1-B-E-2	20-AUG-2012 15:14	HK1222046-016	<0.5	<1	<20			
M2-S-E-1	20-AUG-2012 15:26	HK1222046-017	<0.5	<1	<20			
M2-S-E-2	20-AUG-2012 15:26	HK1222046-018	<0.5	<1	<20			
M2-B-E-1	20-AUG-2012 15:26	HK1222046-019	<0.5	<1	<20			
M2-B-E-2	20-AUG-2012 15:26	HK1222046-020	<0.5	<1	<20			
DM4-S-E-1	20-AUG-2012 15:46	HK1222046-021	<0.5	<1	<20			
DM4-S-E-2	20-AUG-2012 15:46	HK1222046-022	<0.5	<1	<20			
DM4-B-E-1	20-AUG-2012 15:46	HK1222046-023	<0.5	<1	<20			
DM4-B-E-2	20-AUG-2012 15:46	HK1222046-024	<0.5	<1	<20			



Laboratory Duplicate (DUP) Report

Matrix: WATER				Laboratory Duplicate (DUP) Report				
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	LOR	Unit	Original Result	Duplicate Result	RPD (%)
EG: Metals and Major Cations - Filtered (QC Lot: 2463252)								
HK1221672-022	Anonymous	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
HK1222046-007	M2-B-F-1	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463253)								
HK1221672-022	Anonymous	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
HK1222046-007	M2-B-F-1	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463254)								
HK1222046-018	M2-S-E-2	EG020: Cadmium	7440-43-9	0.5	µg/L	<0.5	<0.5	0.0
		EG020: Chromium	7440-47-3	1	µg/L	<1	<1	0.0
EG: Metals and Major Cations - Filtered (QC Lot: 2463255)								
HK1222046-018	M2-S-E-2	EG020: Aluminium	7429-90-5	20	µg/L	<20	<20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: WATER				Method Blank (MB) Report		Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report					
Method: Compound	CAS Number	LOR	Unit	Result	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
						LCS	DCS	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2463252)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	93.4	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	92.0	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2463253)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	106	----	85	115	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2463254)											
EG020: Cadmium	7440-43-9	0.2	µg/L	<0.2	10 µg/L	104	----	80	112	----	----
EG020: Chromium	7440-47-3	1	µg/L	<1	10 µg/L	103	----	80	114	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2463255)											
EG020: Aluminium	7429-90-5	10	µg/L	<10	10 µg/L	114	----	85	115	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

Matrix: WATER				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2463252)										
HK1221672-021	Anonymous	EG020: Cadmium	7440-43-9	10 µg/L	106	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	98.7	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2463253)										
HK1221672-021	Anonymous	EG020: Aluminium	7429-90-5	10 µg/L	102	----	75	125	----	----



Matrix: WATER

				Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report						
Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Spike Concentration	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
					MS	MSD	Low	High	Value	Control Limit
EG: Metals and Major Cations - Filtered (QCLot: 2463254)										
HK1222046-017	M2-S-E-1	EG020: Cadmium	7440-43-9	10 µg/L	109	----	75	125	----	----
		EG020: Chromium	7440-47-3	10 µg/L	101	----	75	125	----	----
EG: Metals and Major Cations - Filtered (QCLot: 2463255)										
HK1222046-017	M2-S-E-1	EG020: Aluminium	7429-90-5	10 µg/L	124	----	75	125	----	----

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 4

Graphical Presentation of Monitoring Data


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - Dissolved Oxygen Content

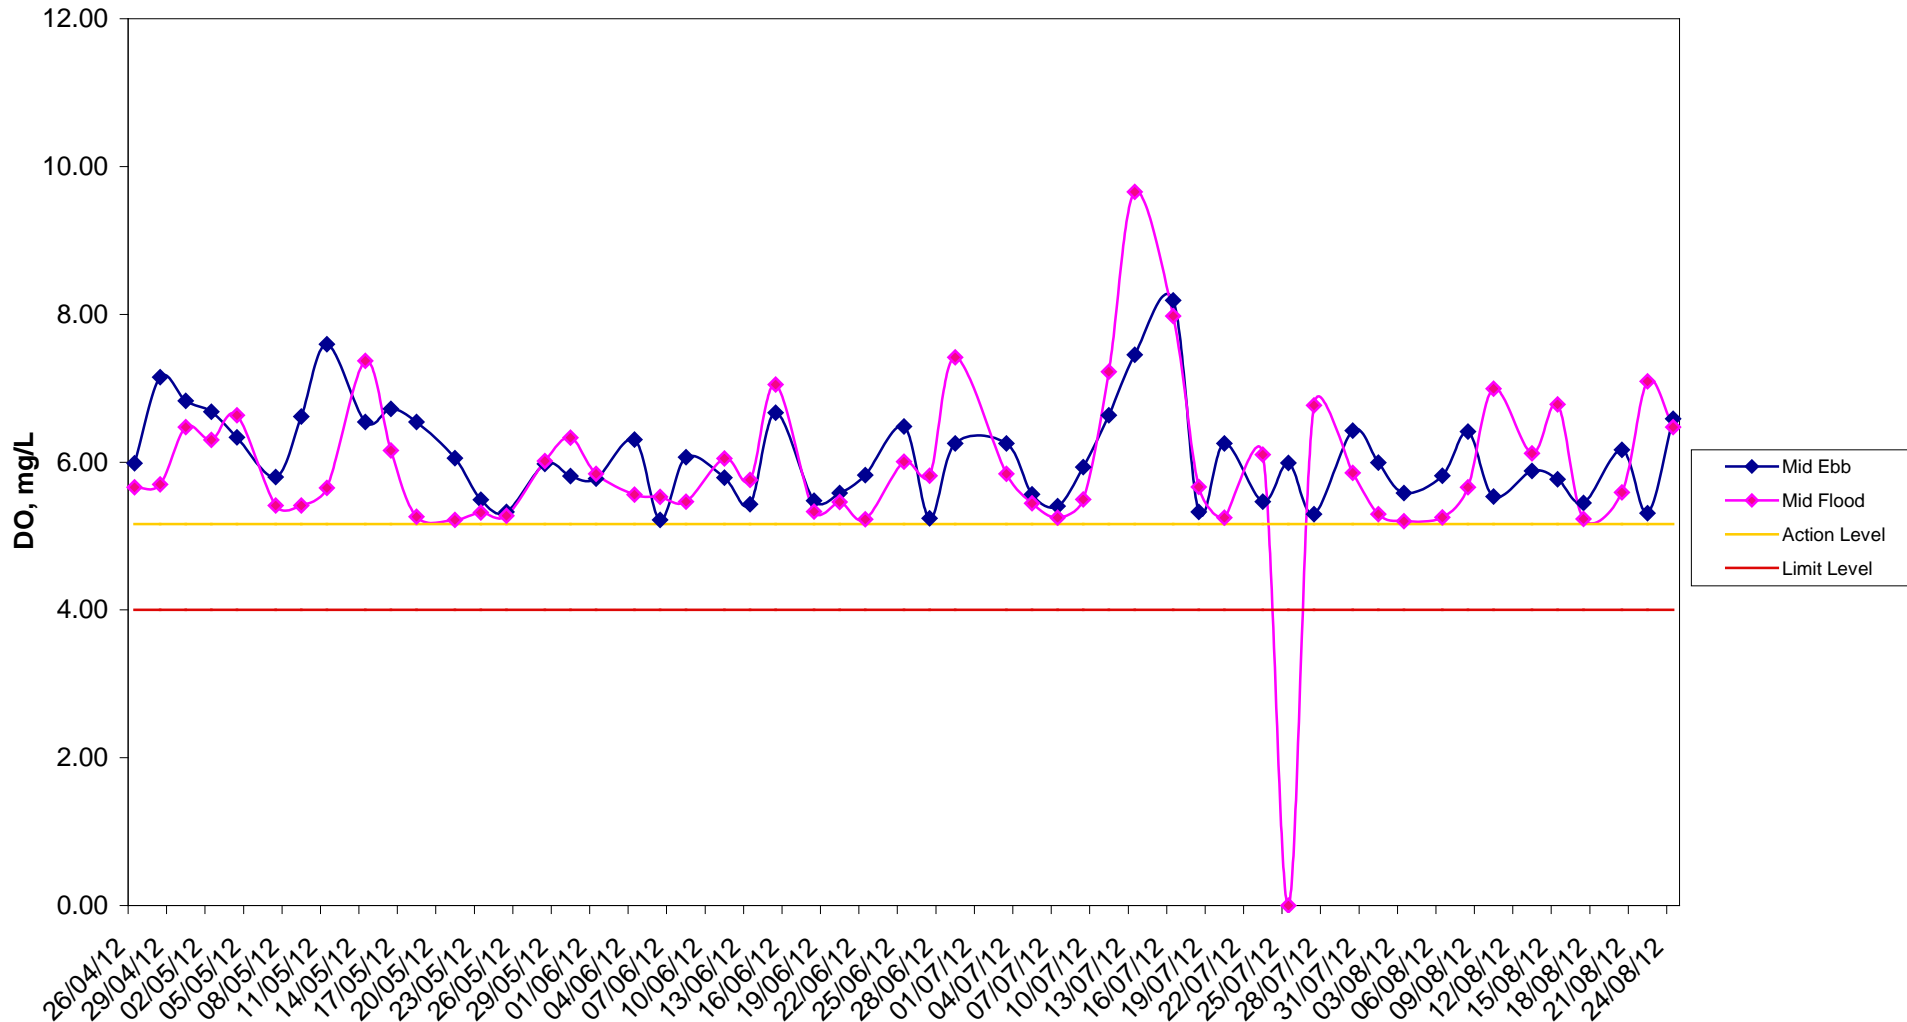


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - Turbidity (Mid-Ebb)

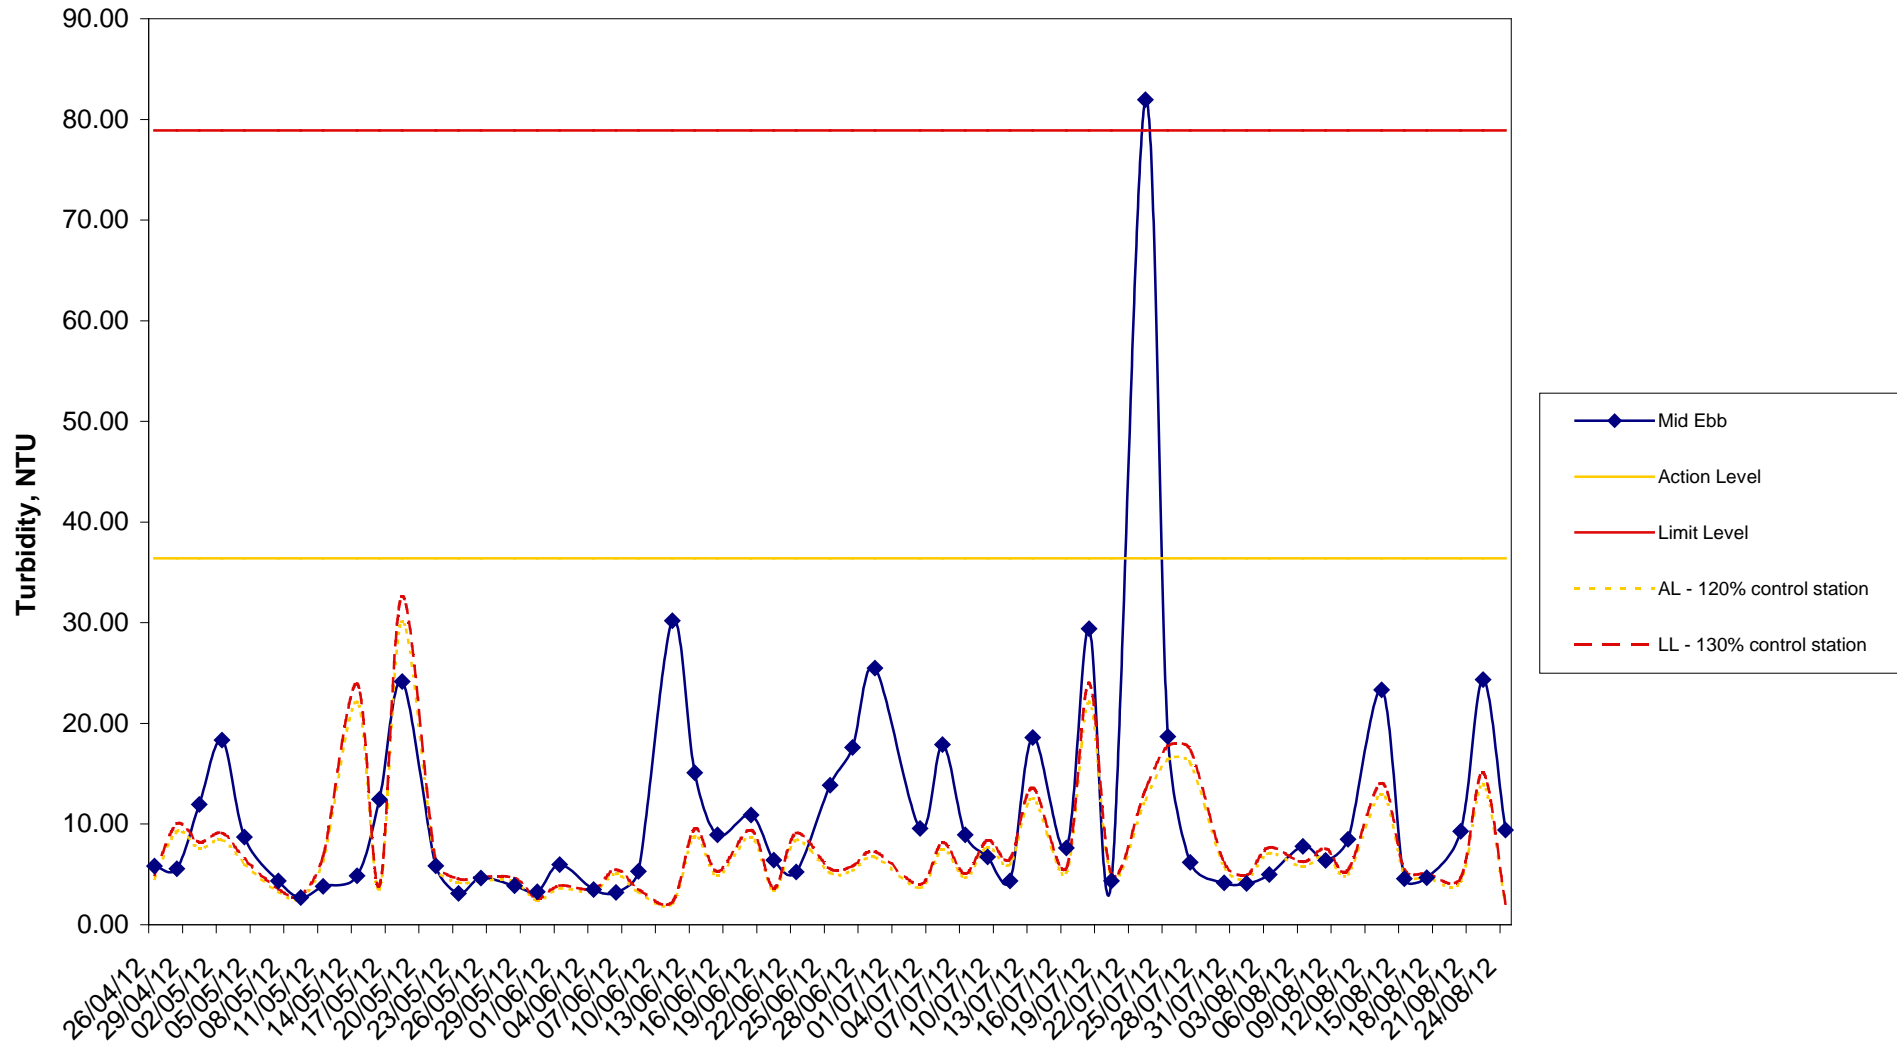


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - Turbidity (Mid-Flood)

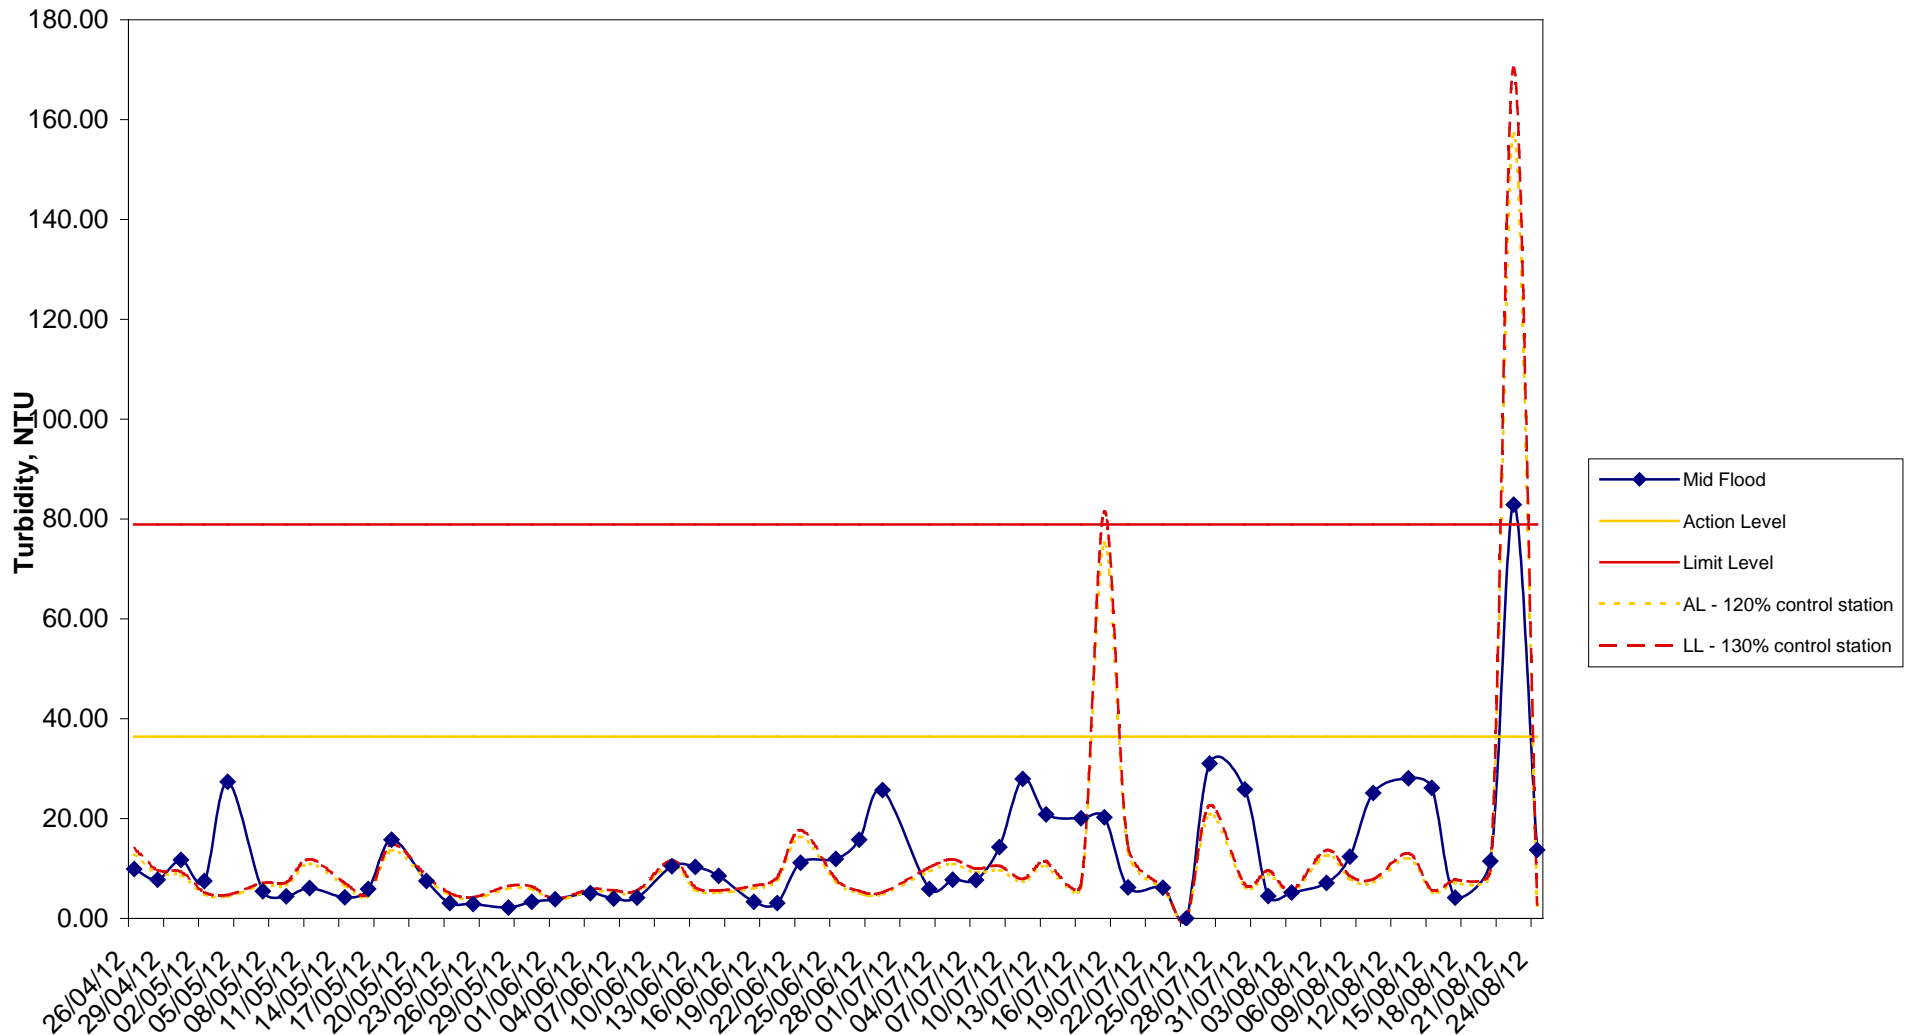


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - pH

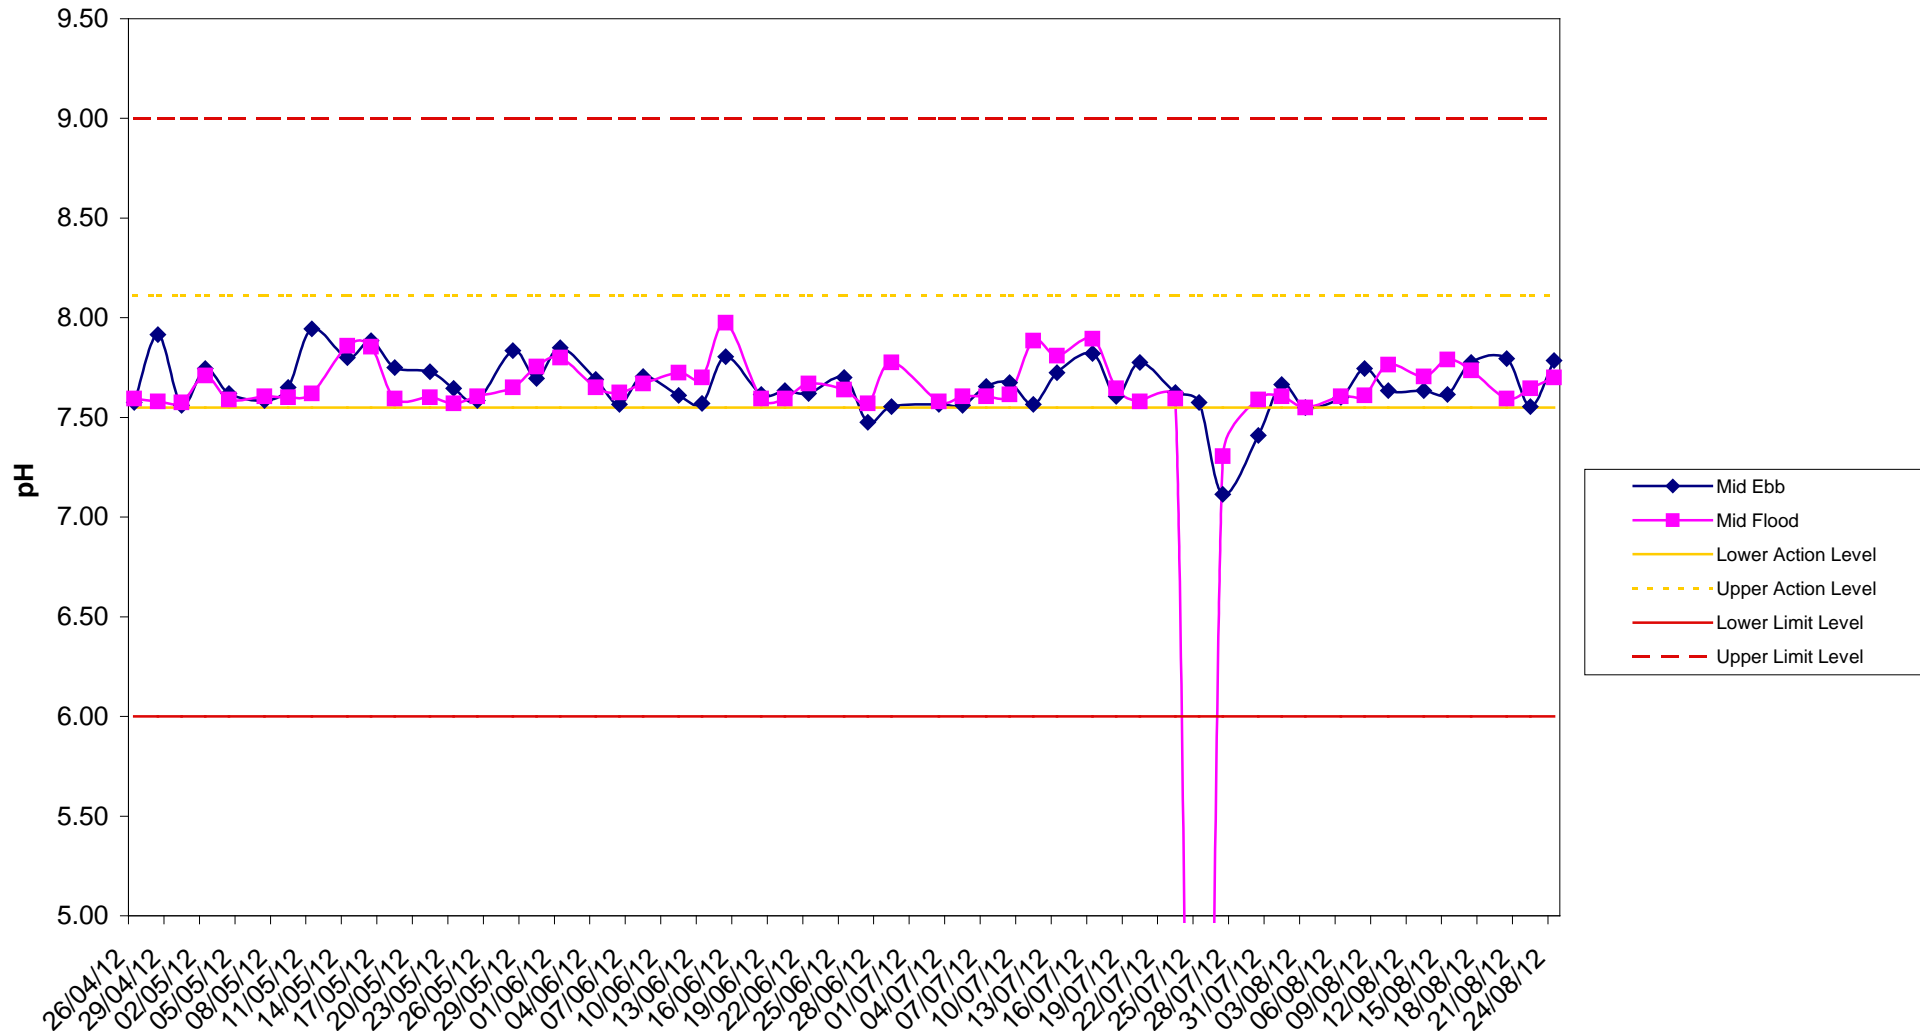


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - Suspended Solid Content (Mid-Ebb)

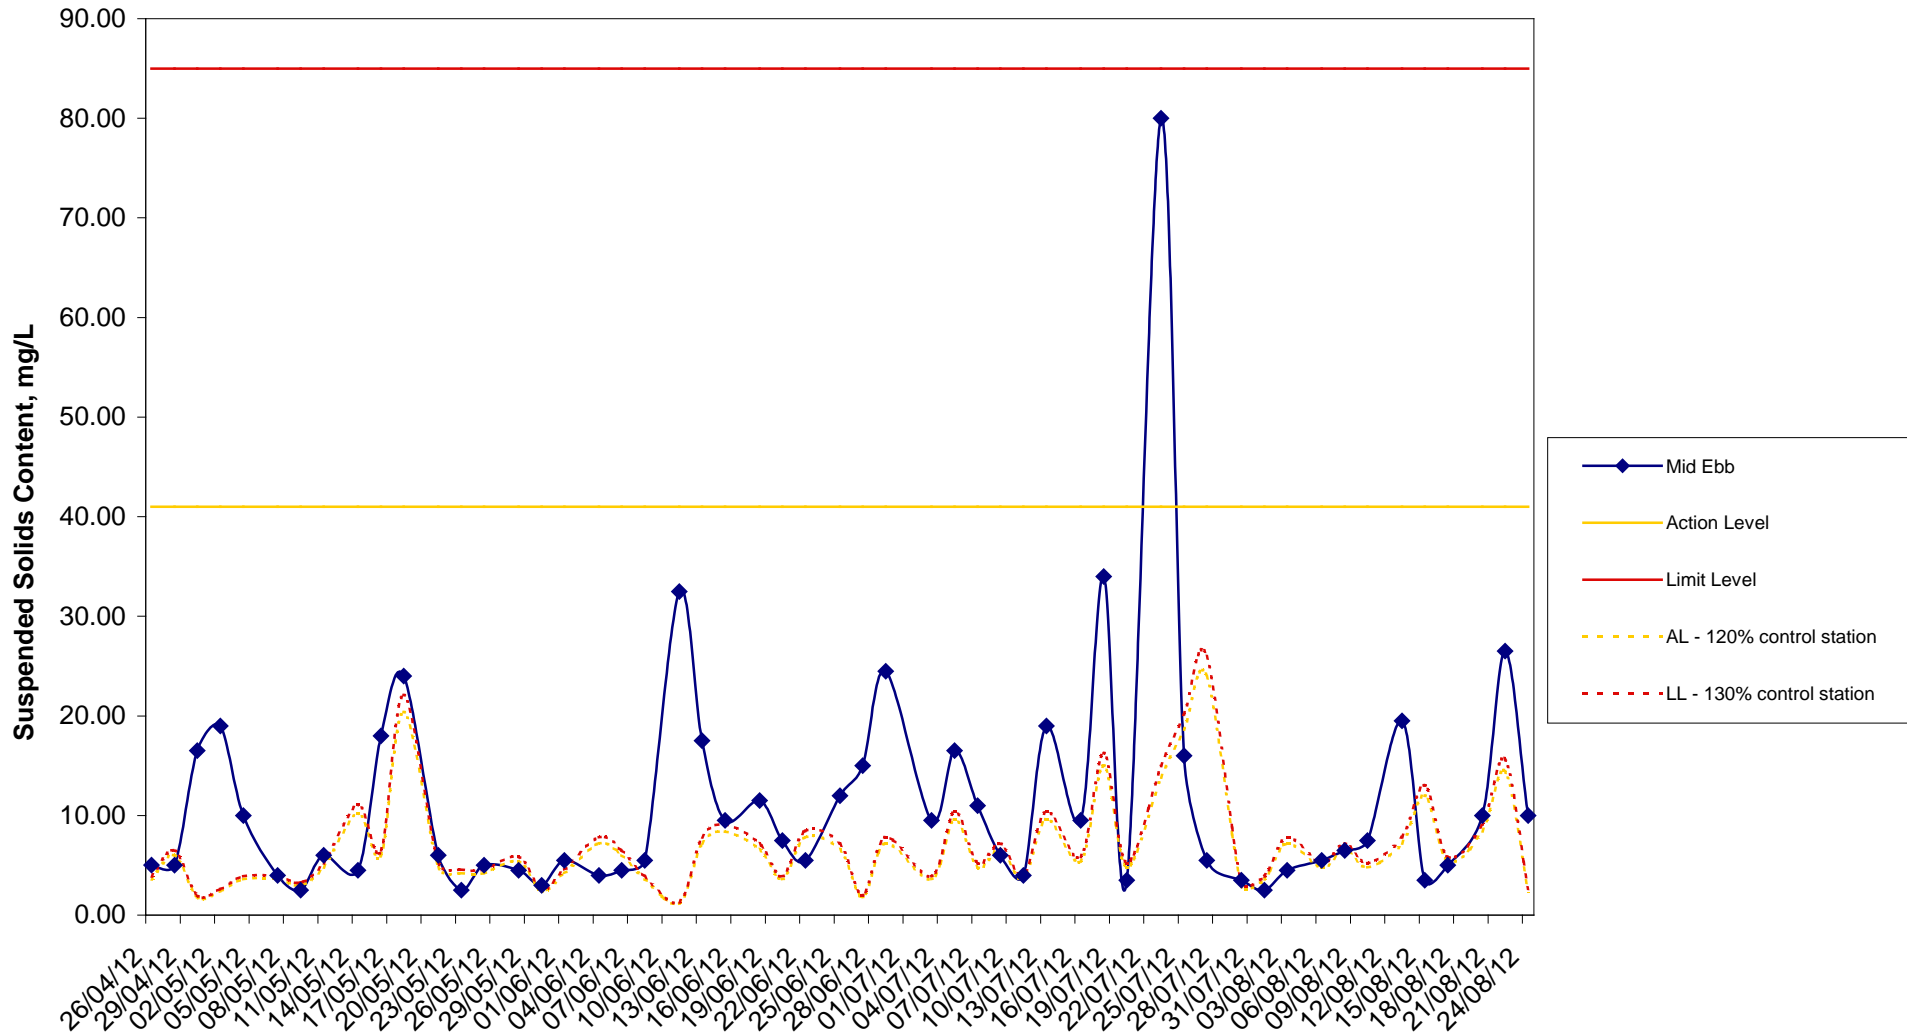


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W1 - Suspended Solids Content (Mid-Flood)

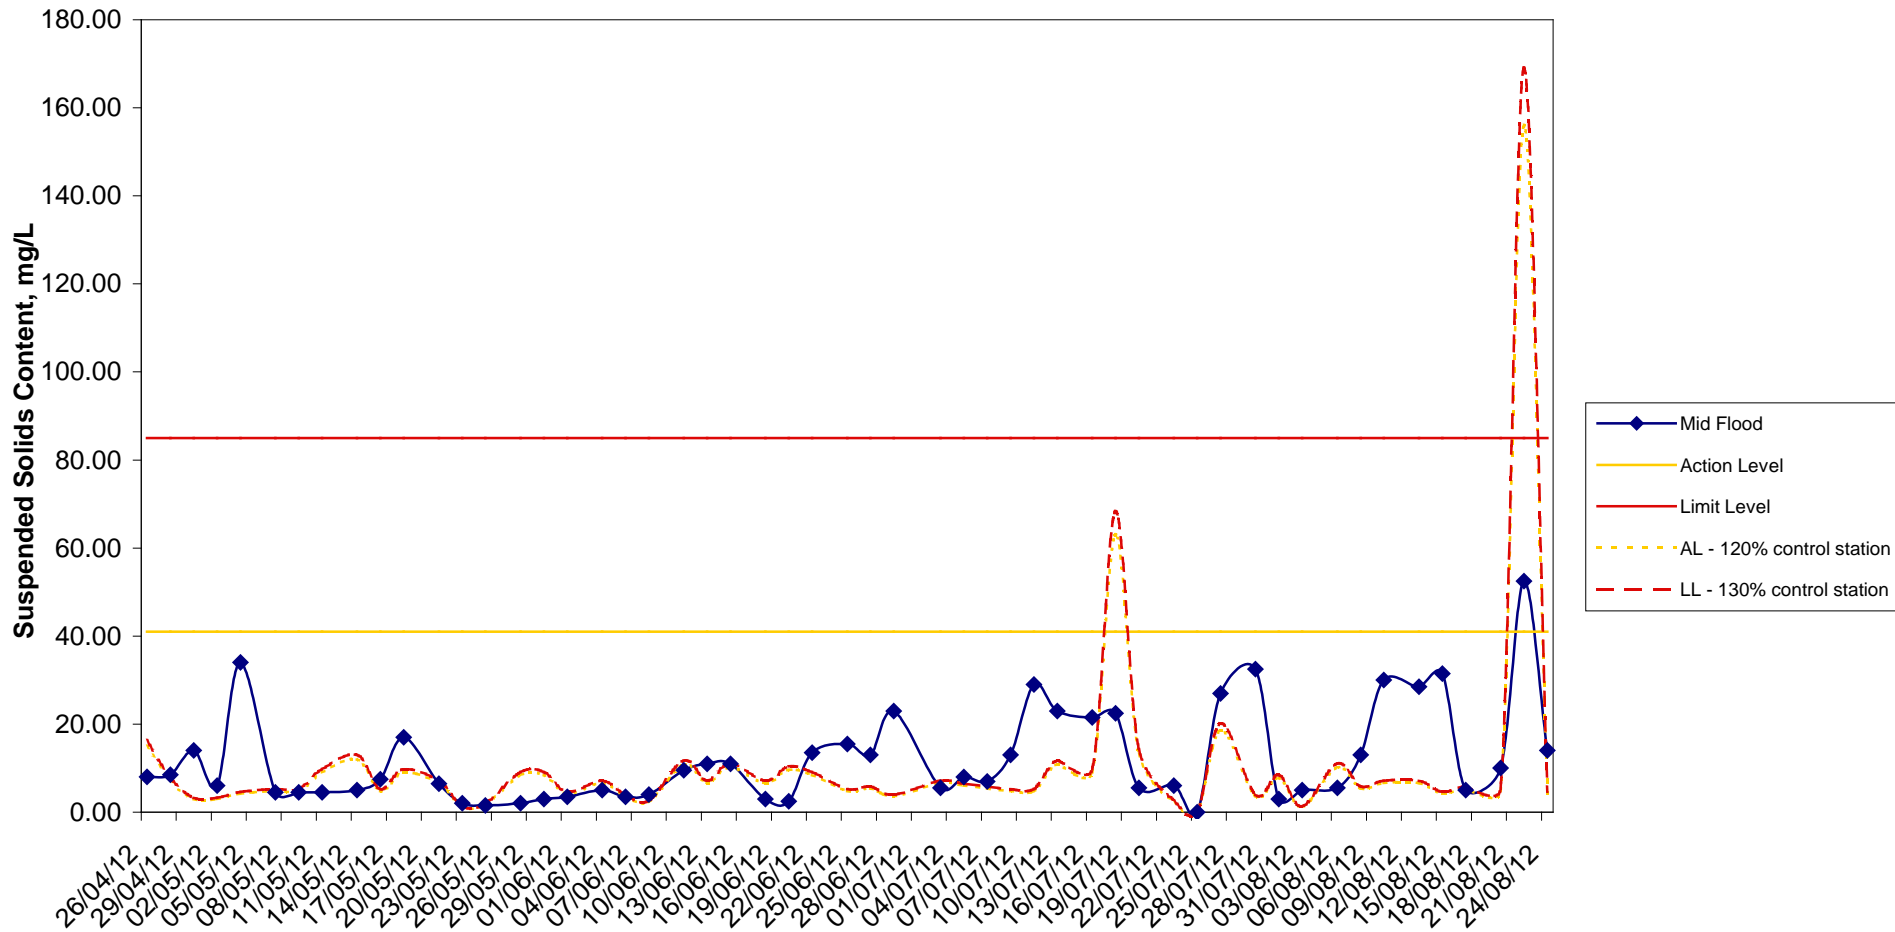


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - Dissolved Oxygen Content

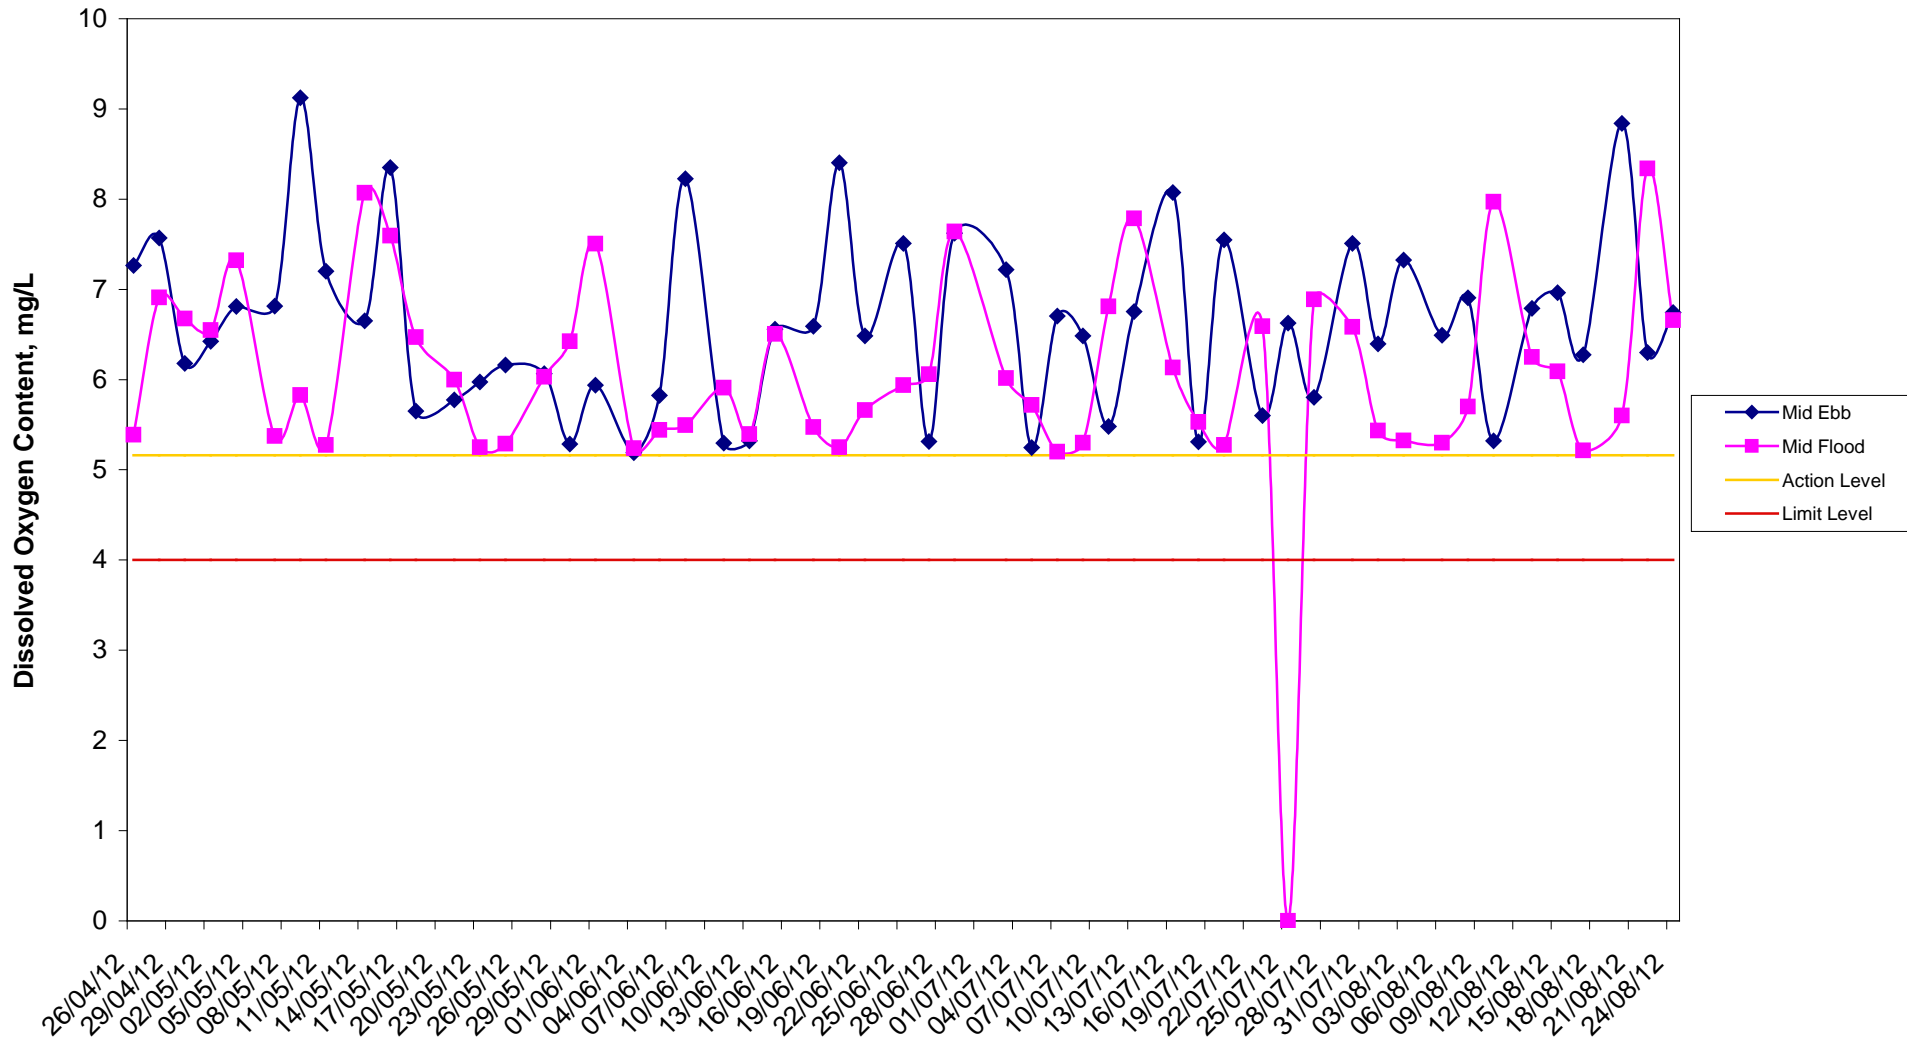


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - Turbidity (Mid-Ebb)

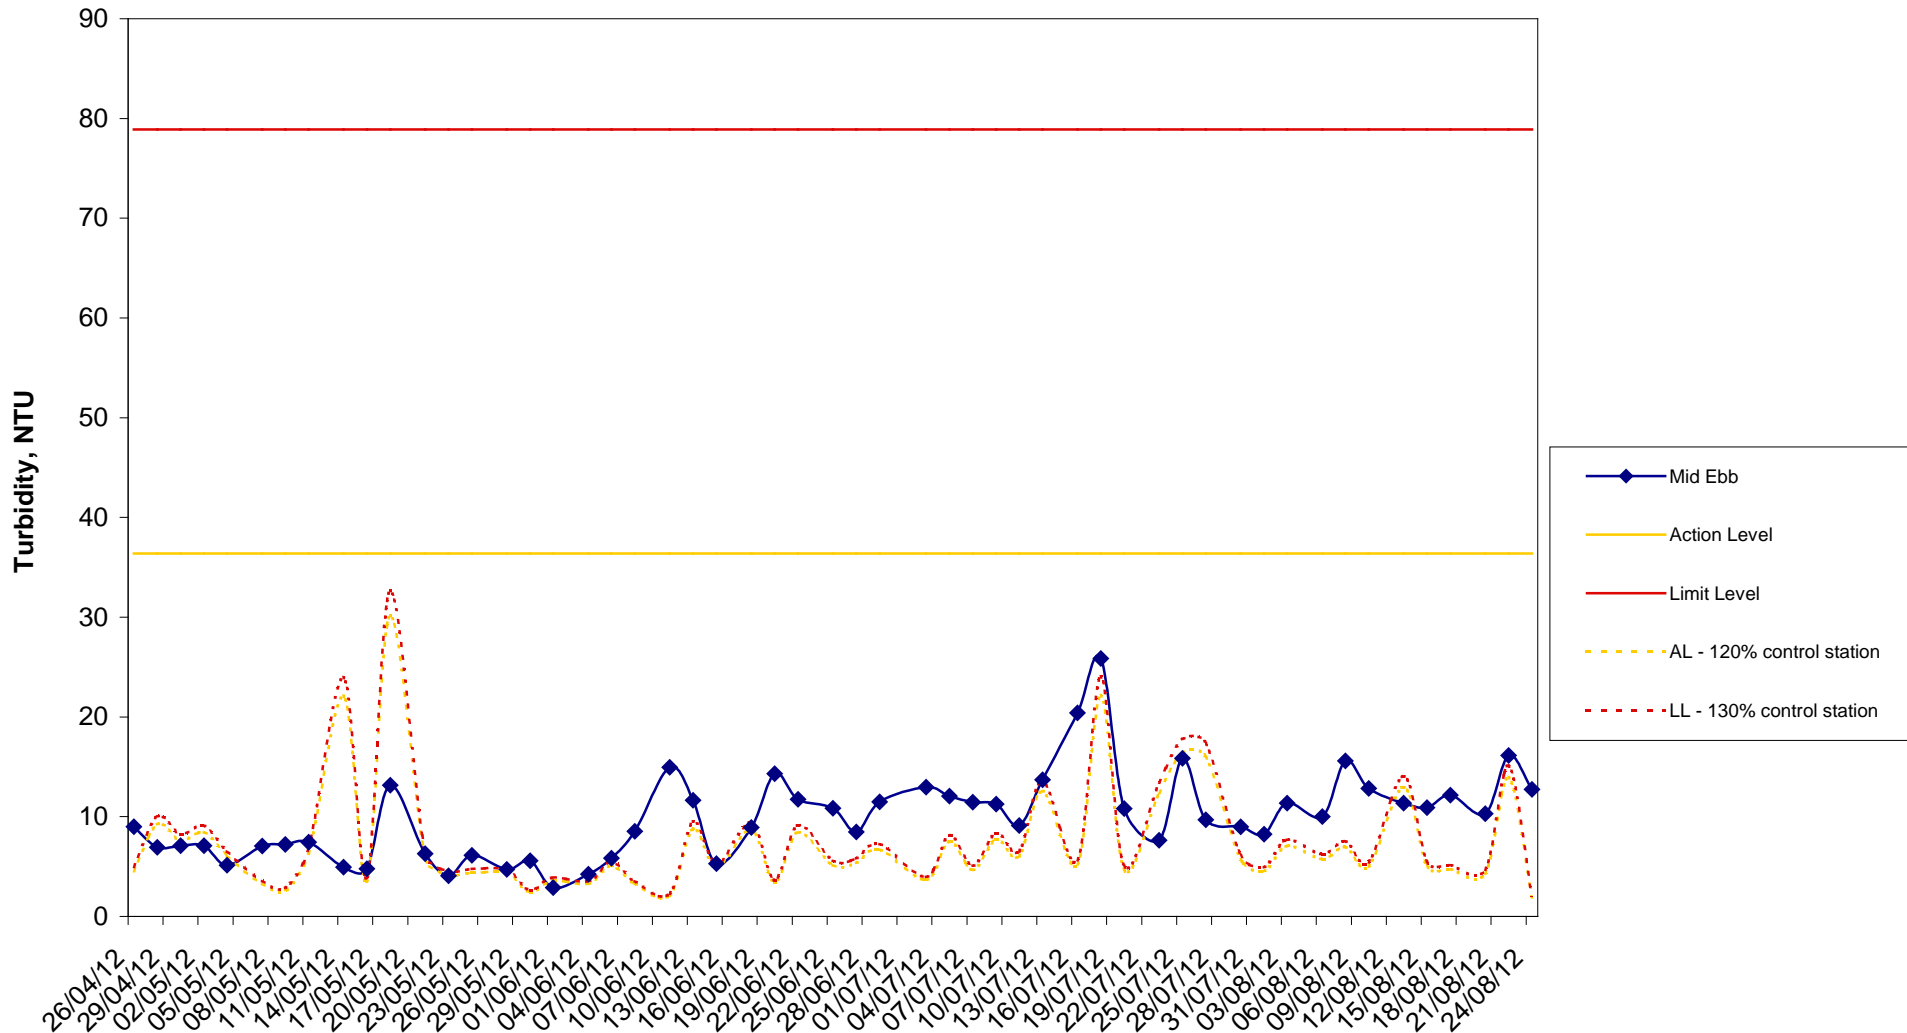


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - Turbidity (Mid-Flood)

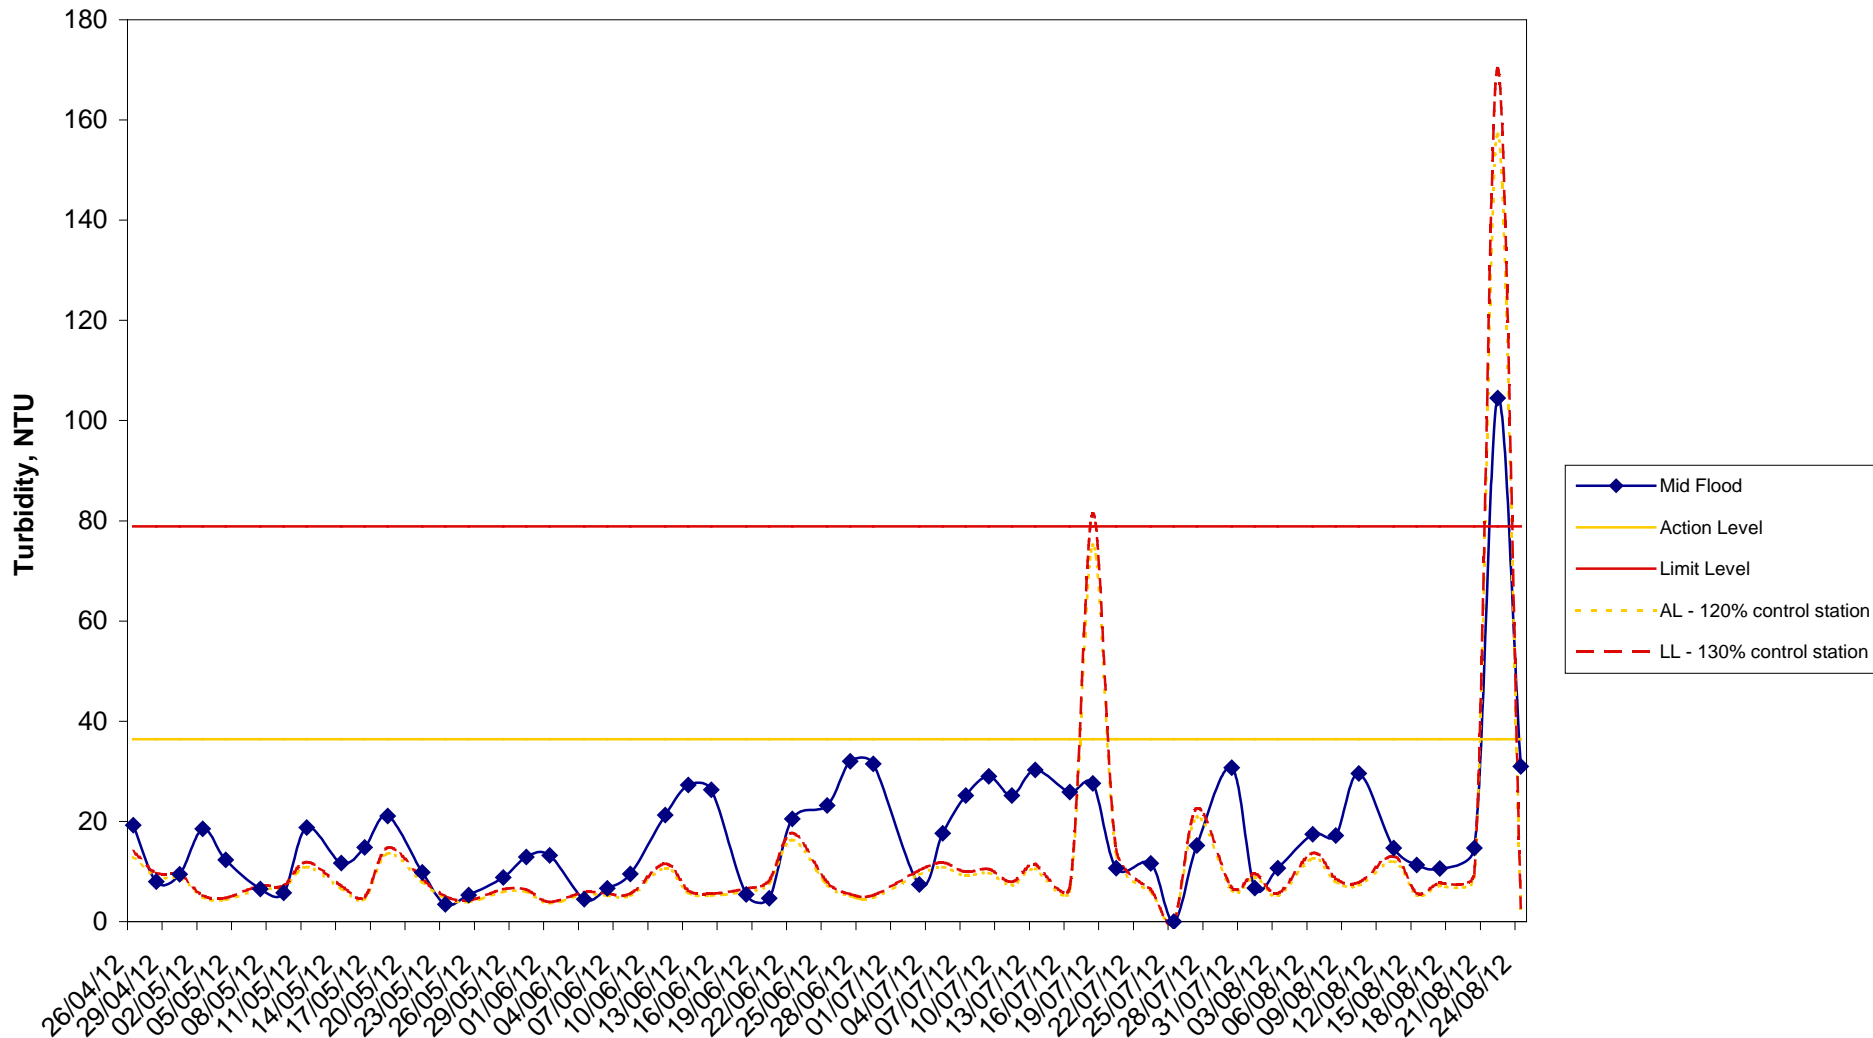


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - pH

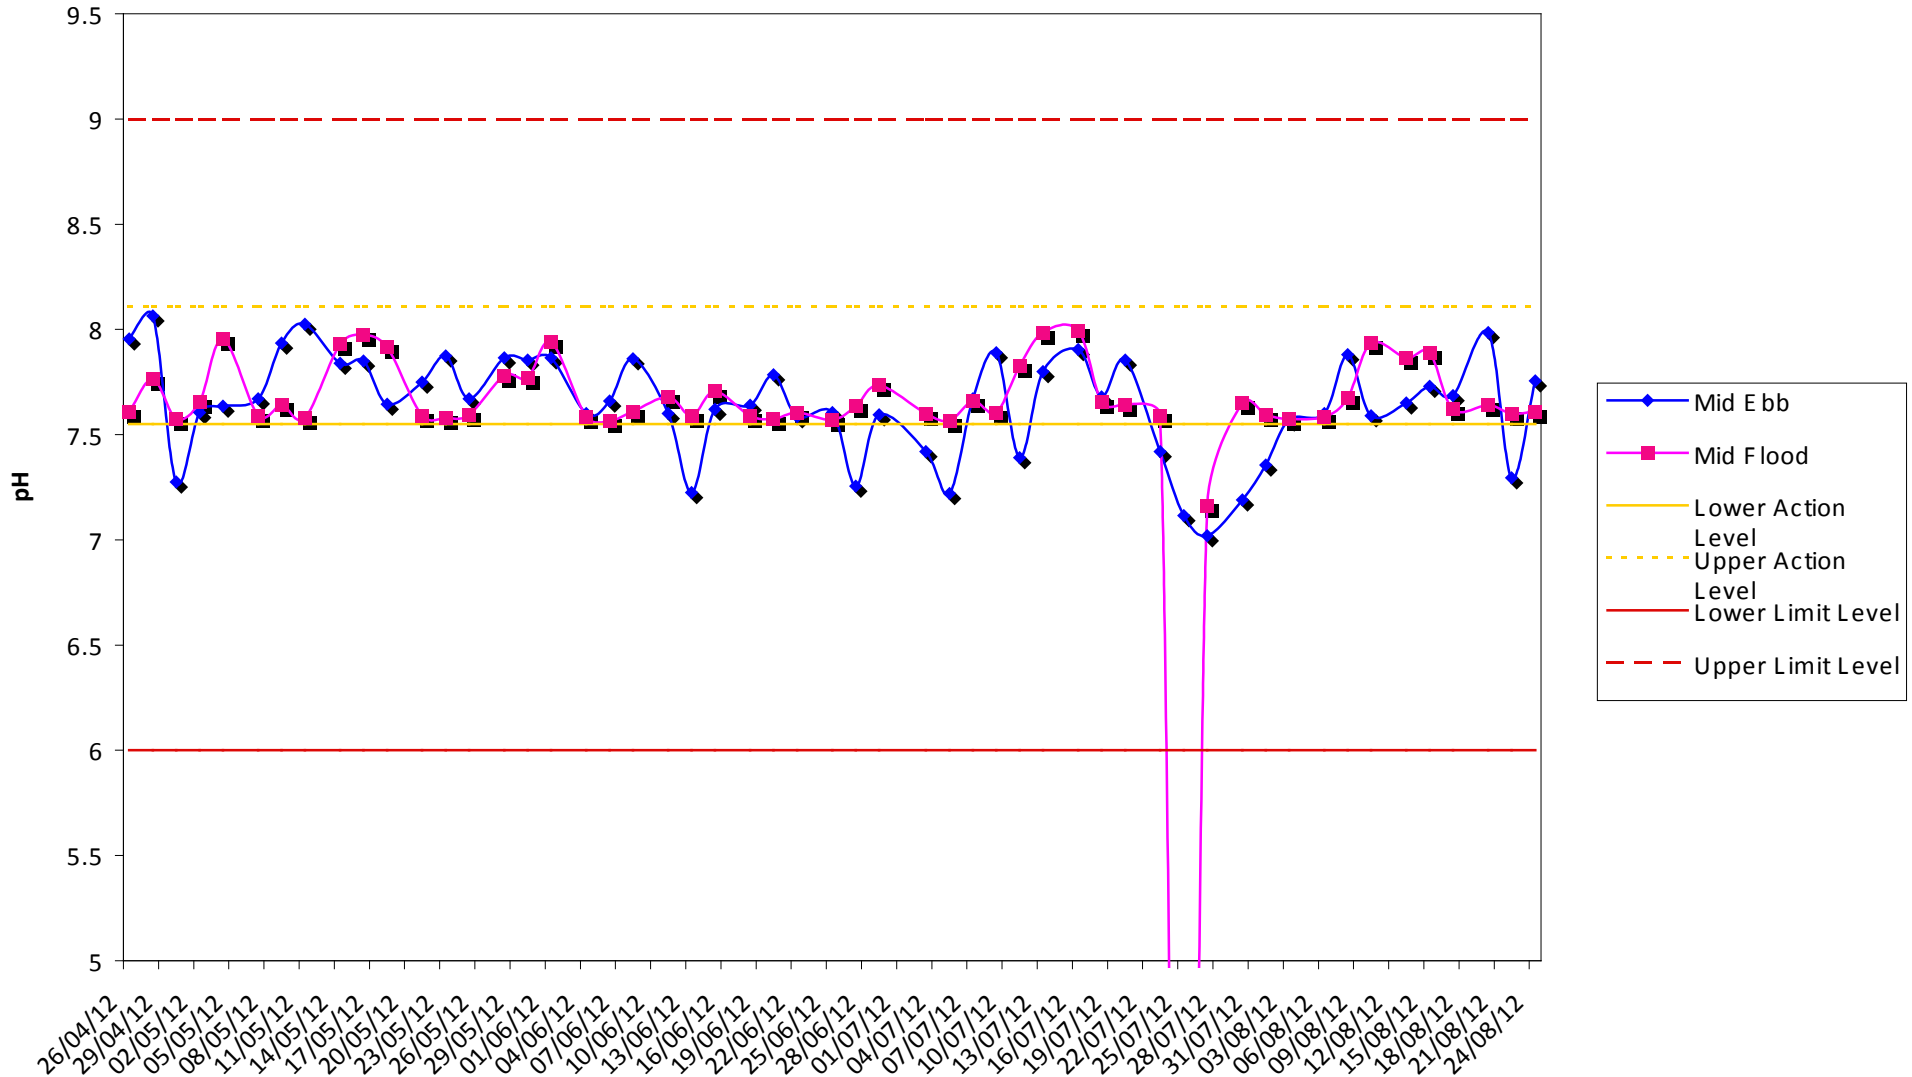


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - Suspended Solids Content (Mid-Ebb)

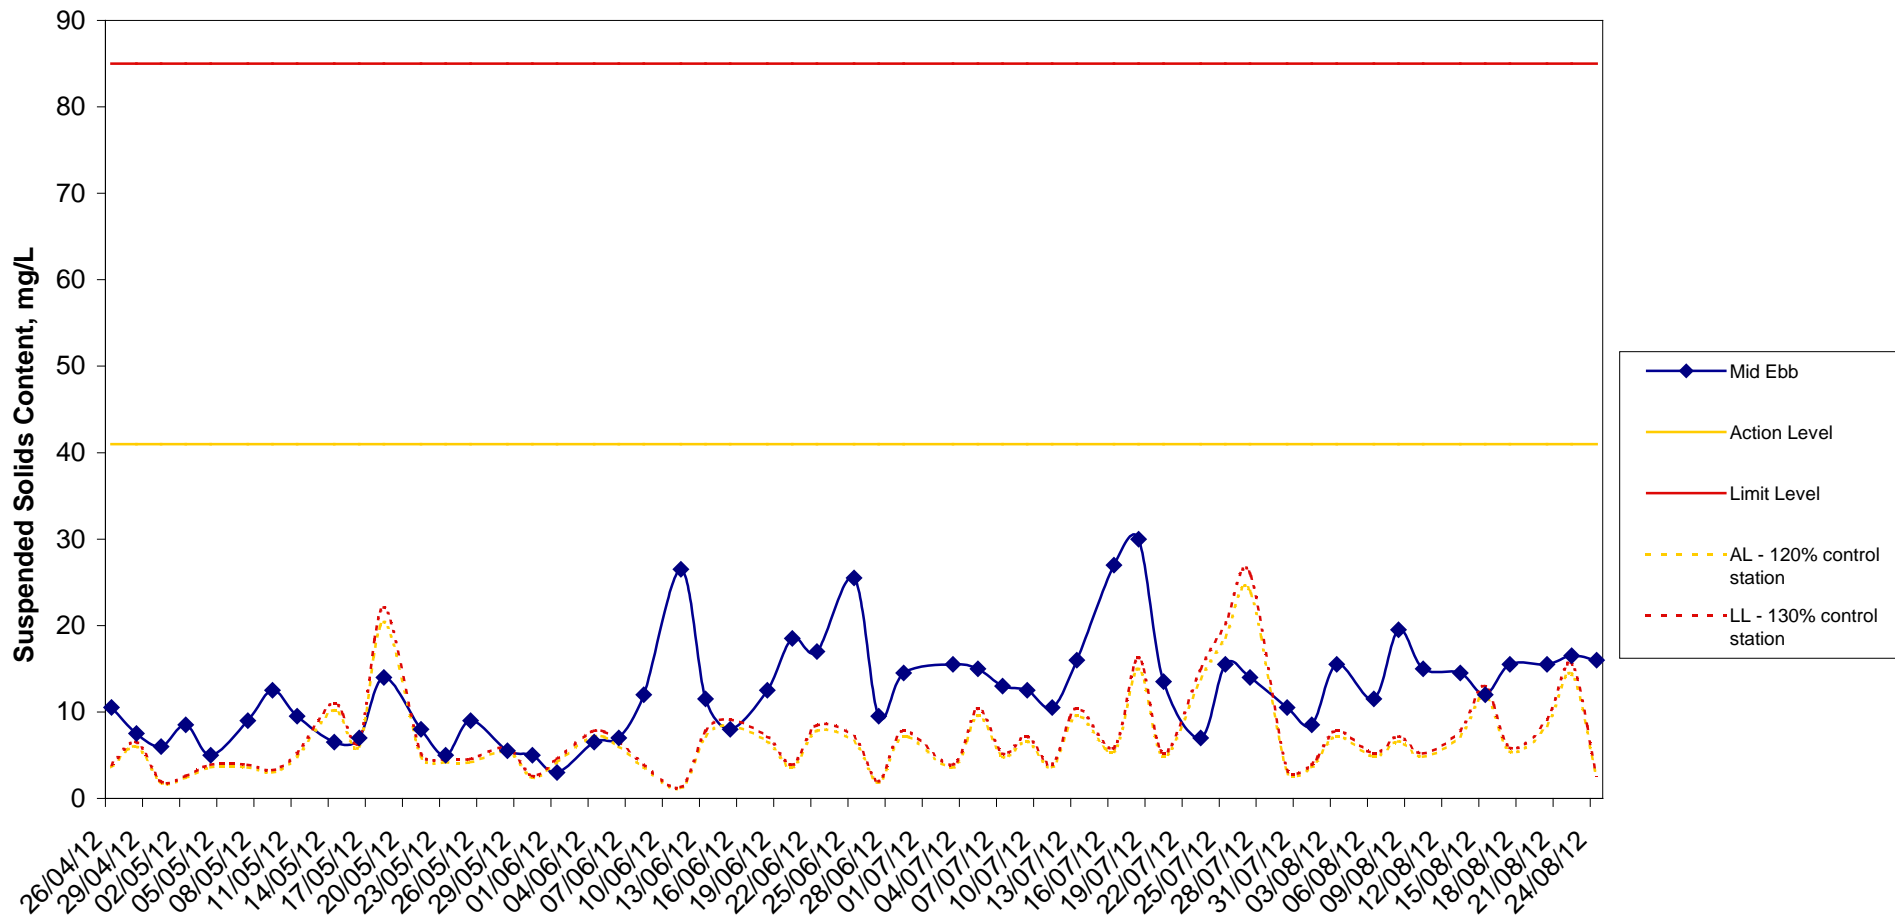


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W2 - Suspended Solids Content (Mid-Flood)

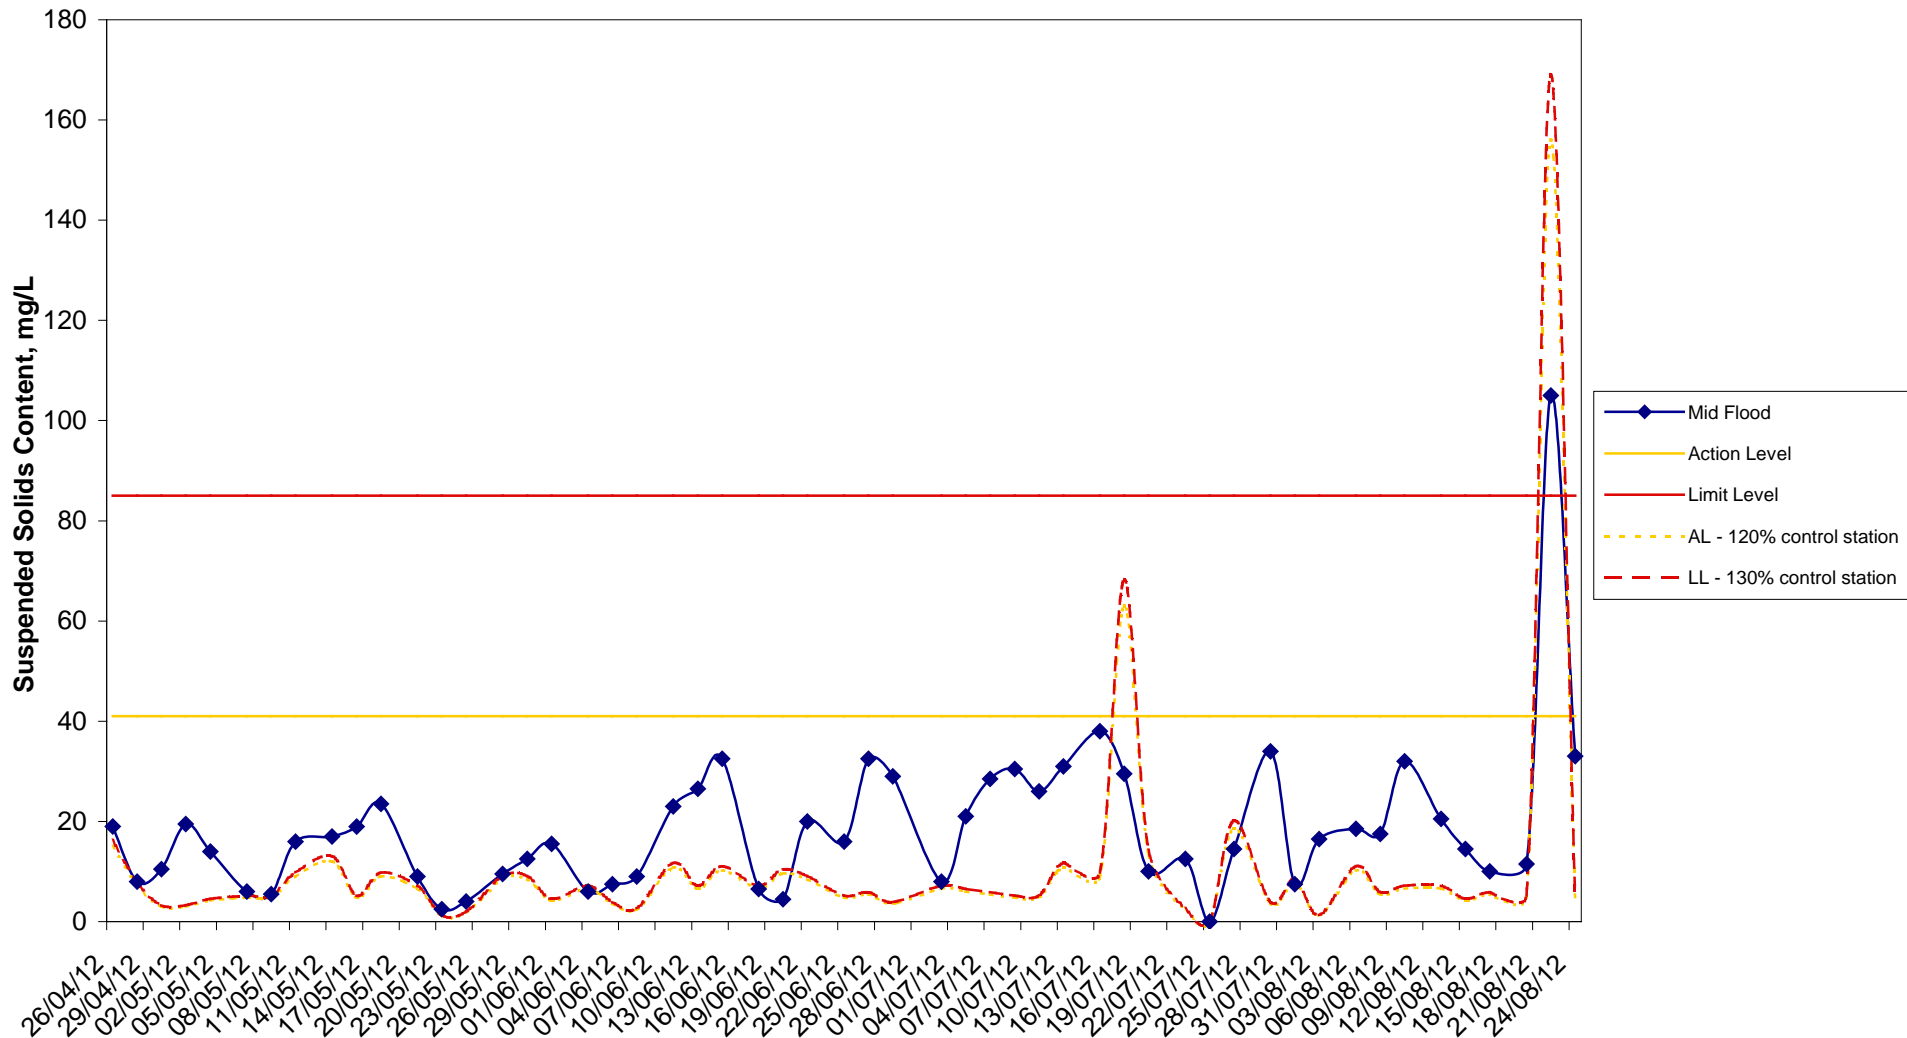


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - Dissolved Oxygen Content

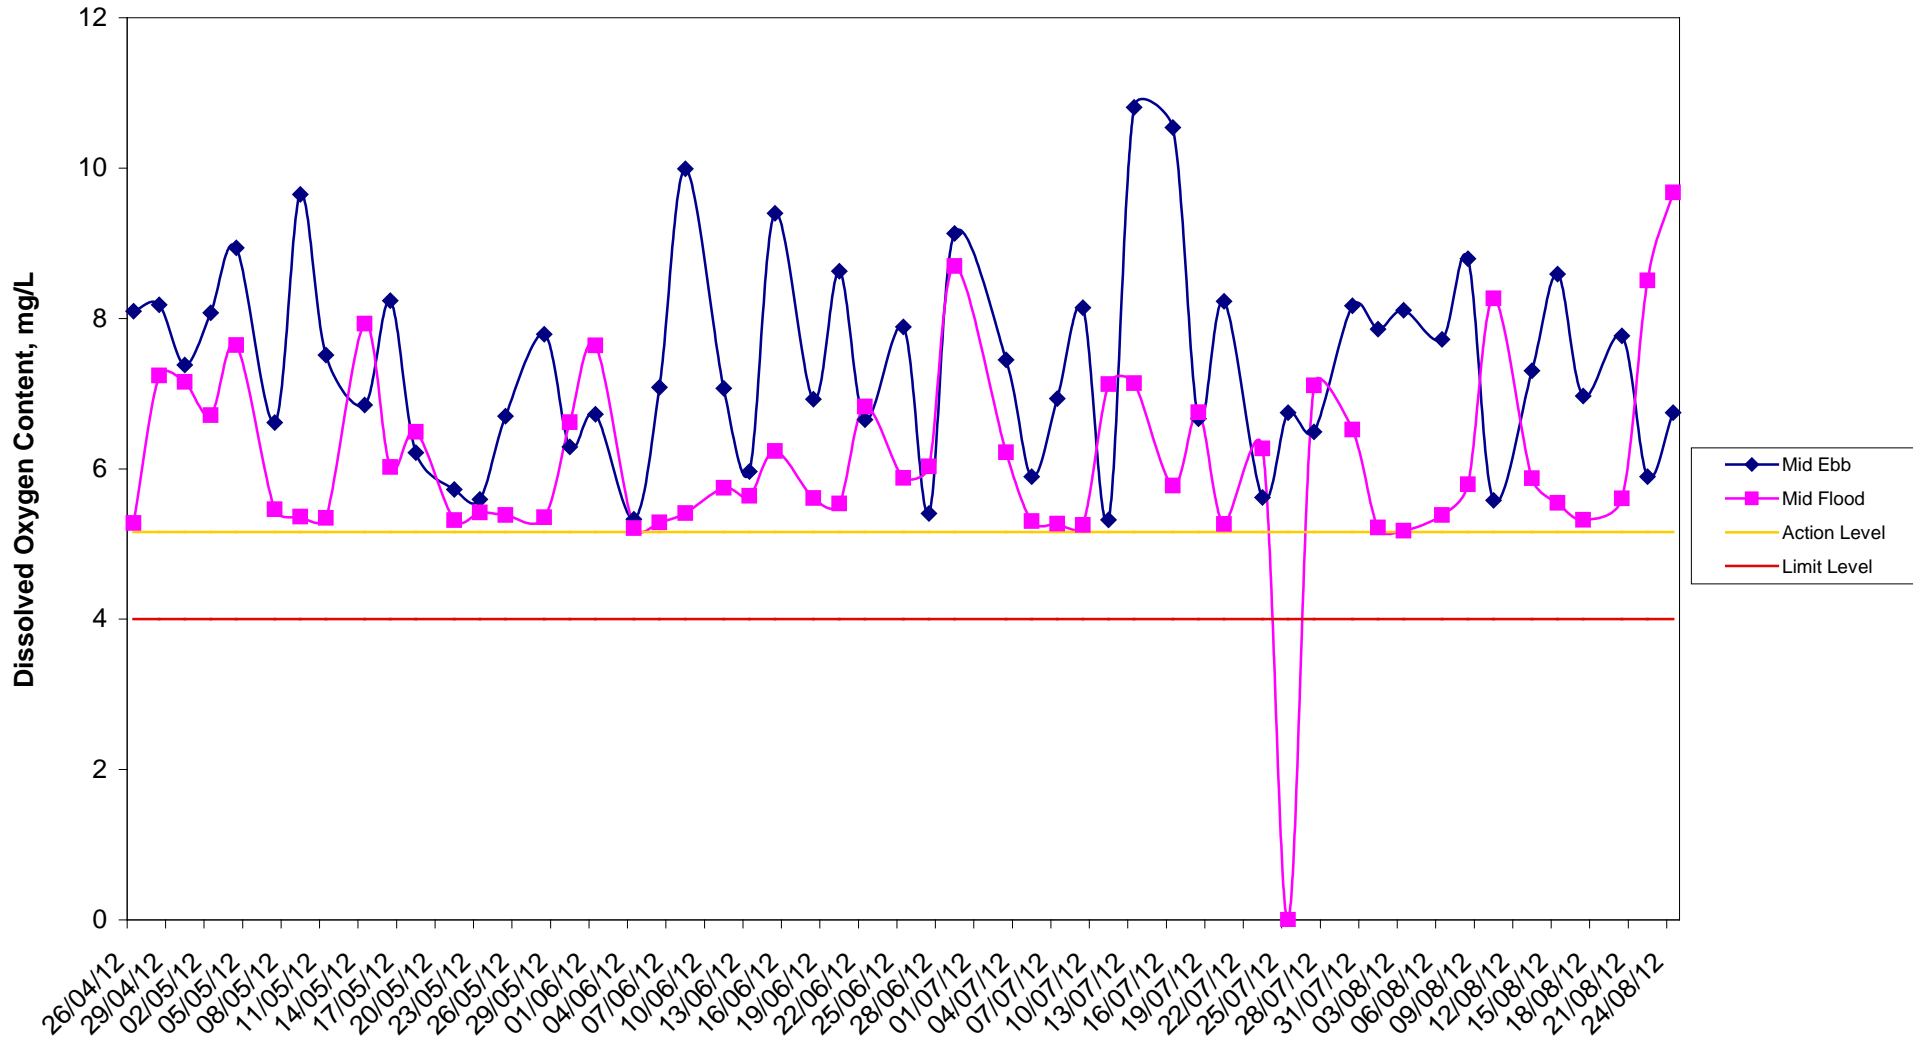


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - Turbidity (Mid-Ebb)

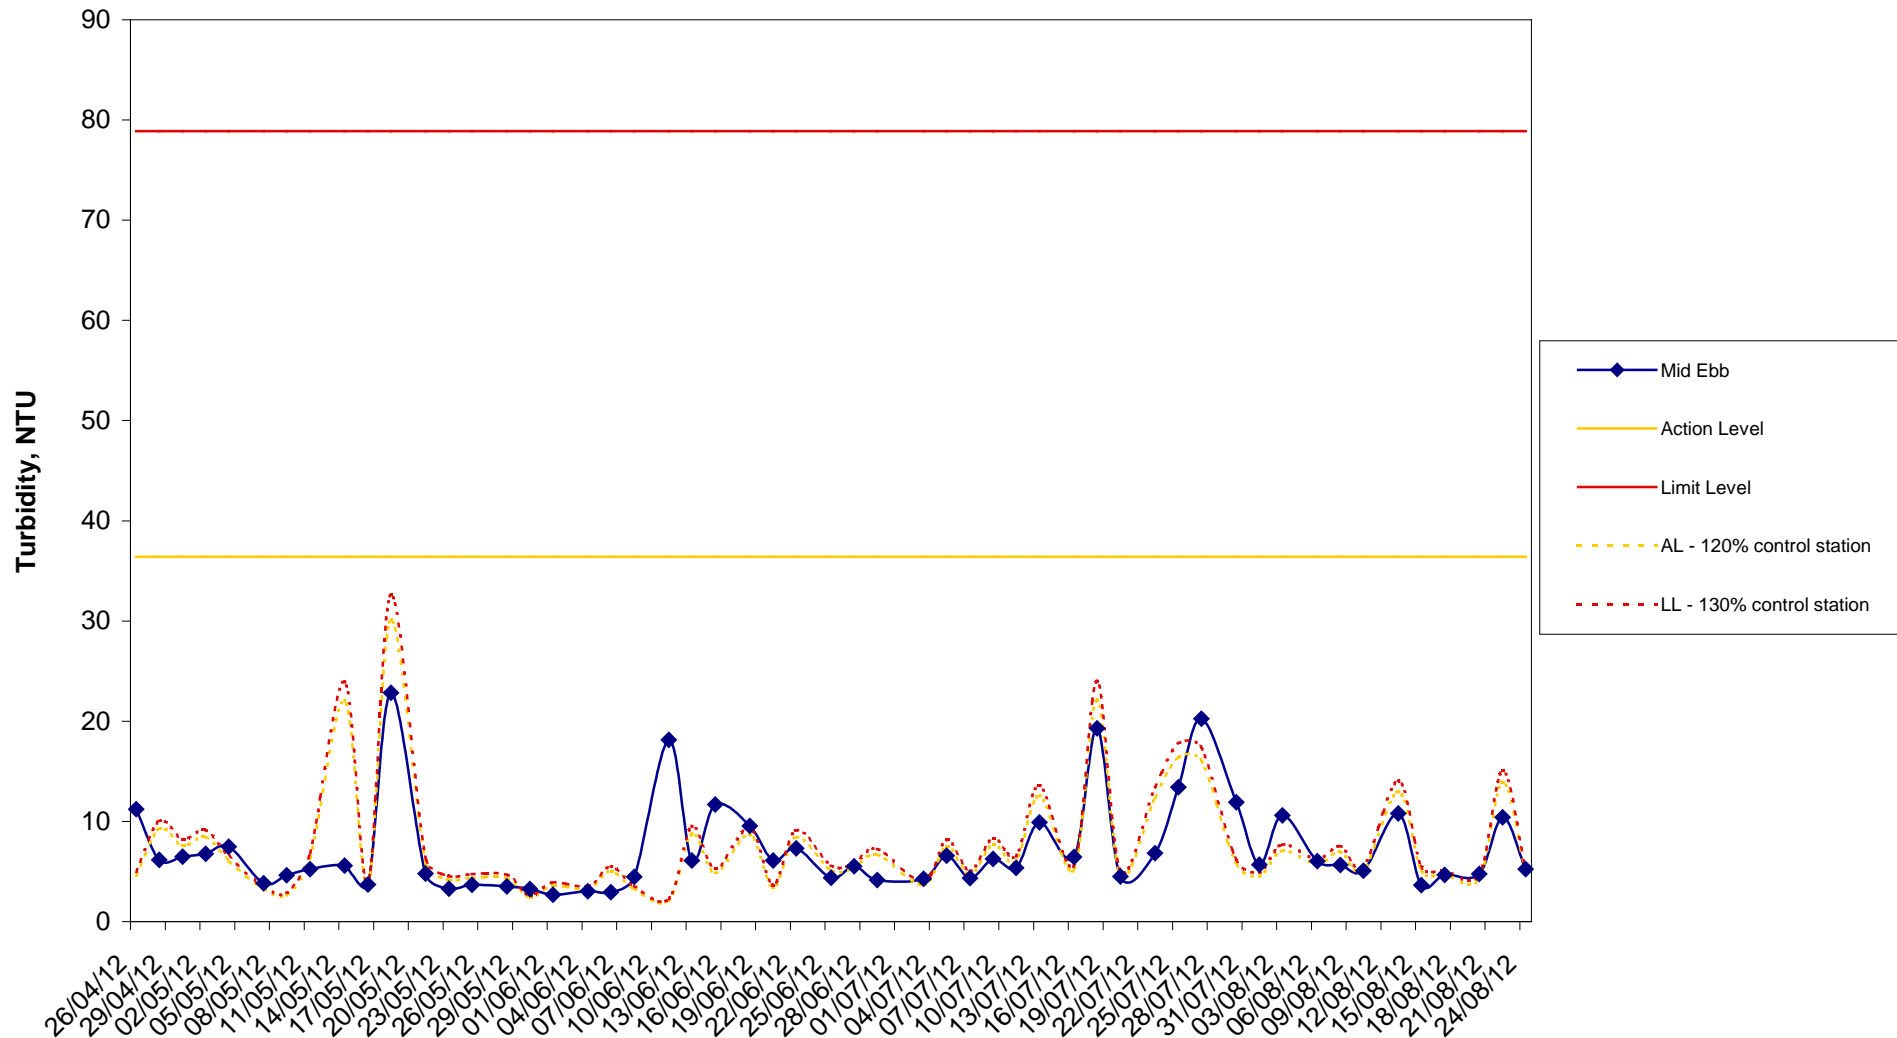


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - Turbidity (Mid-Flood)

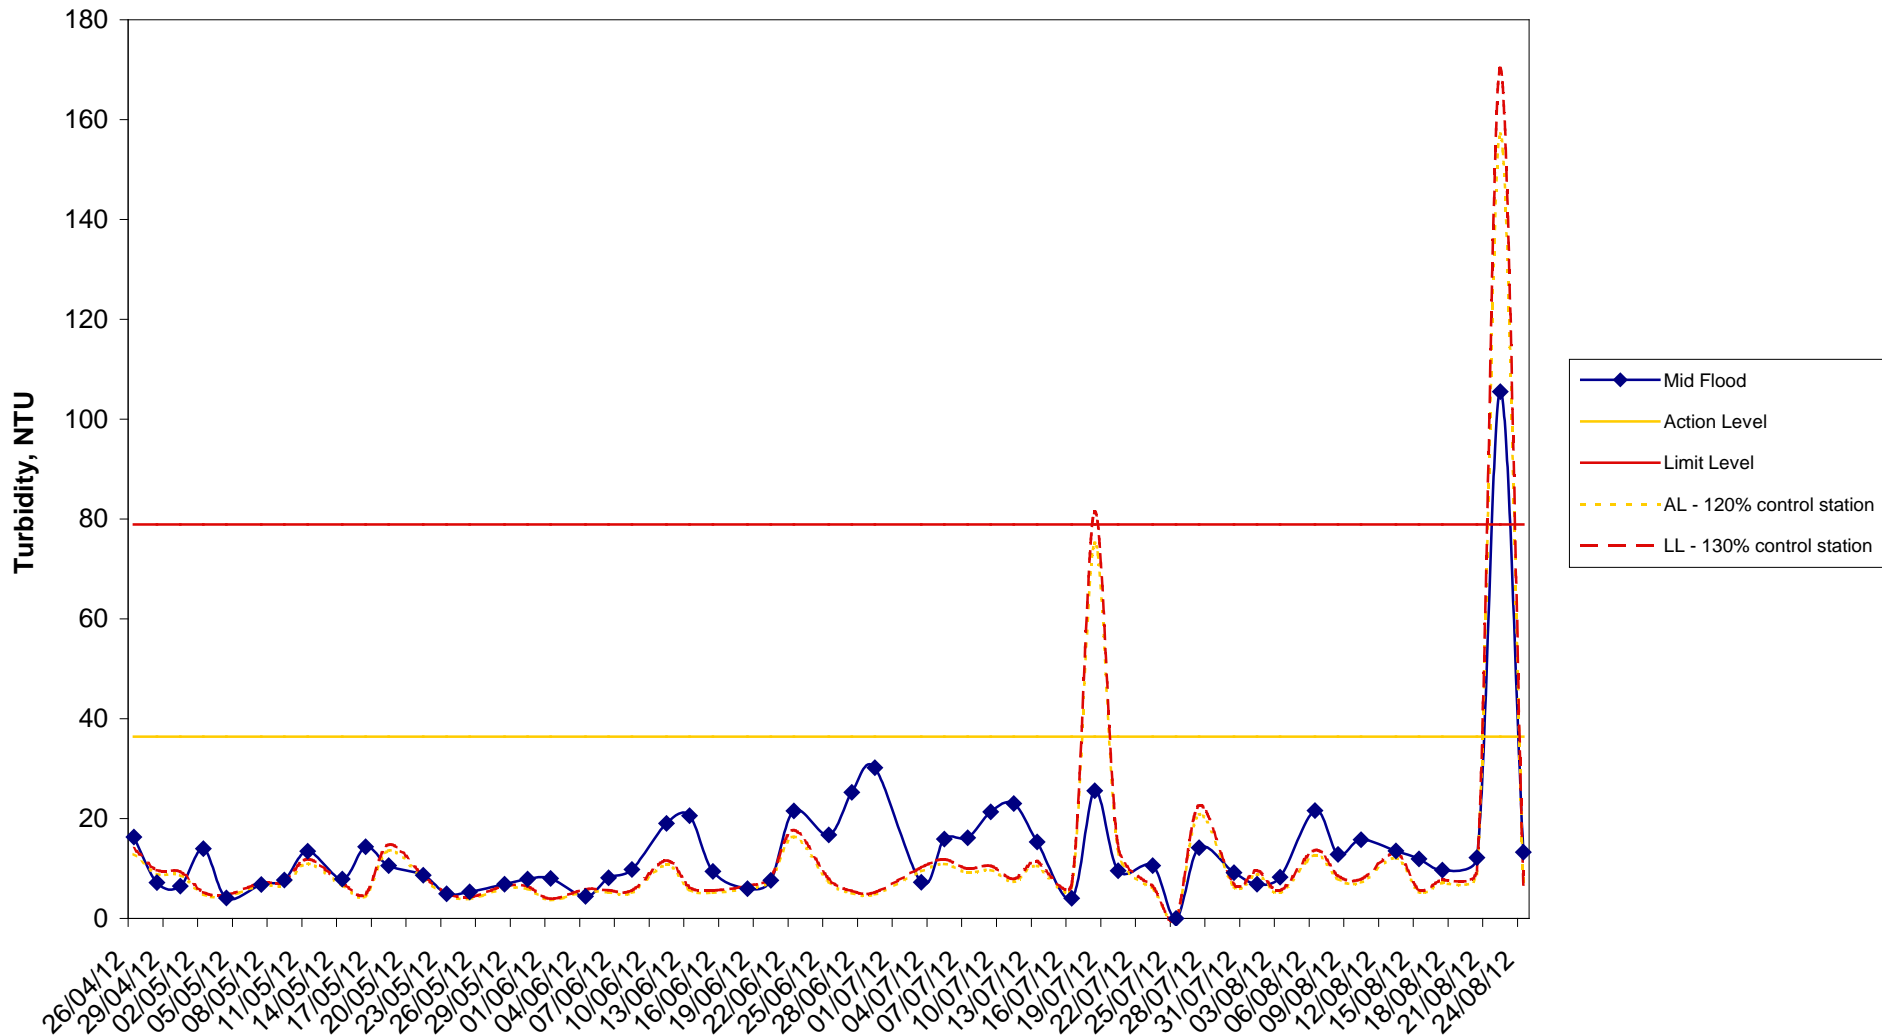


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - pH

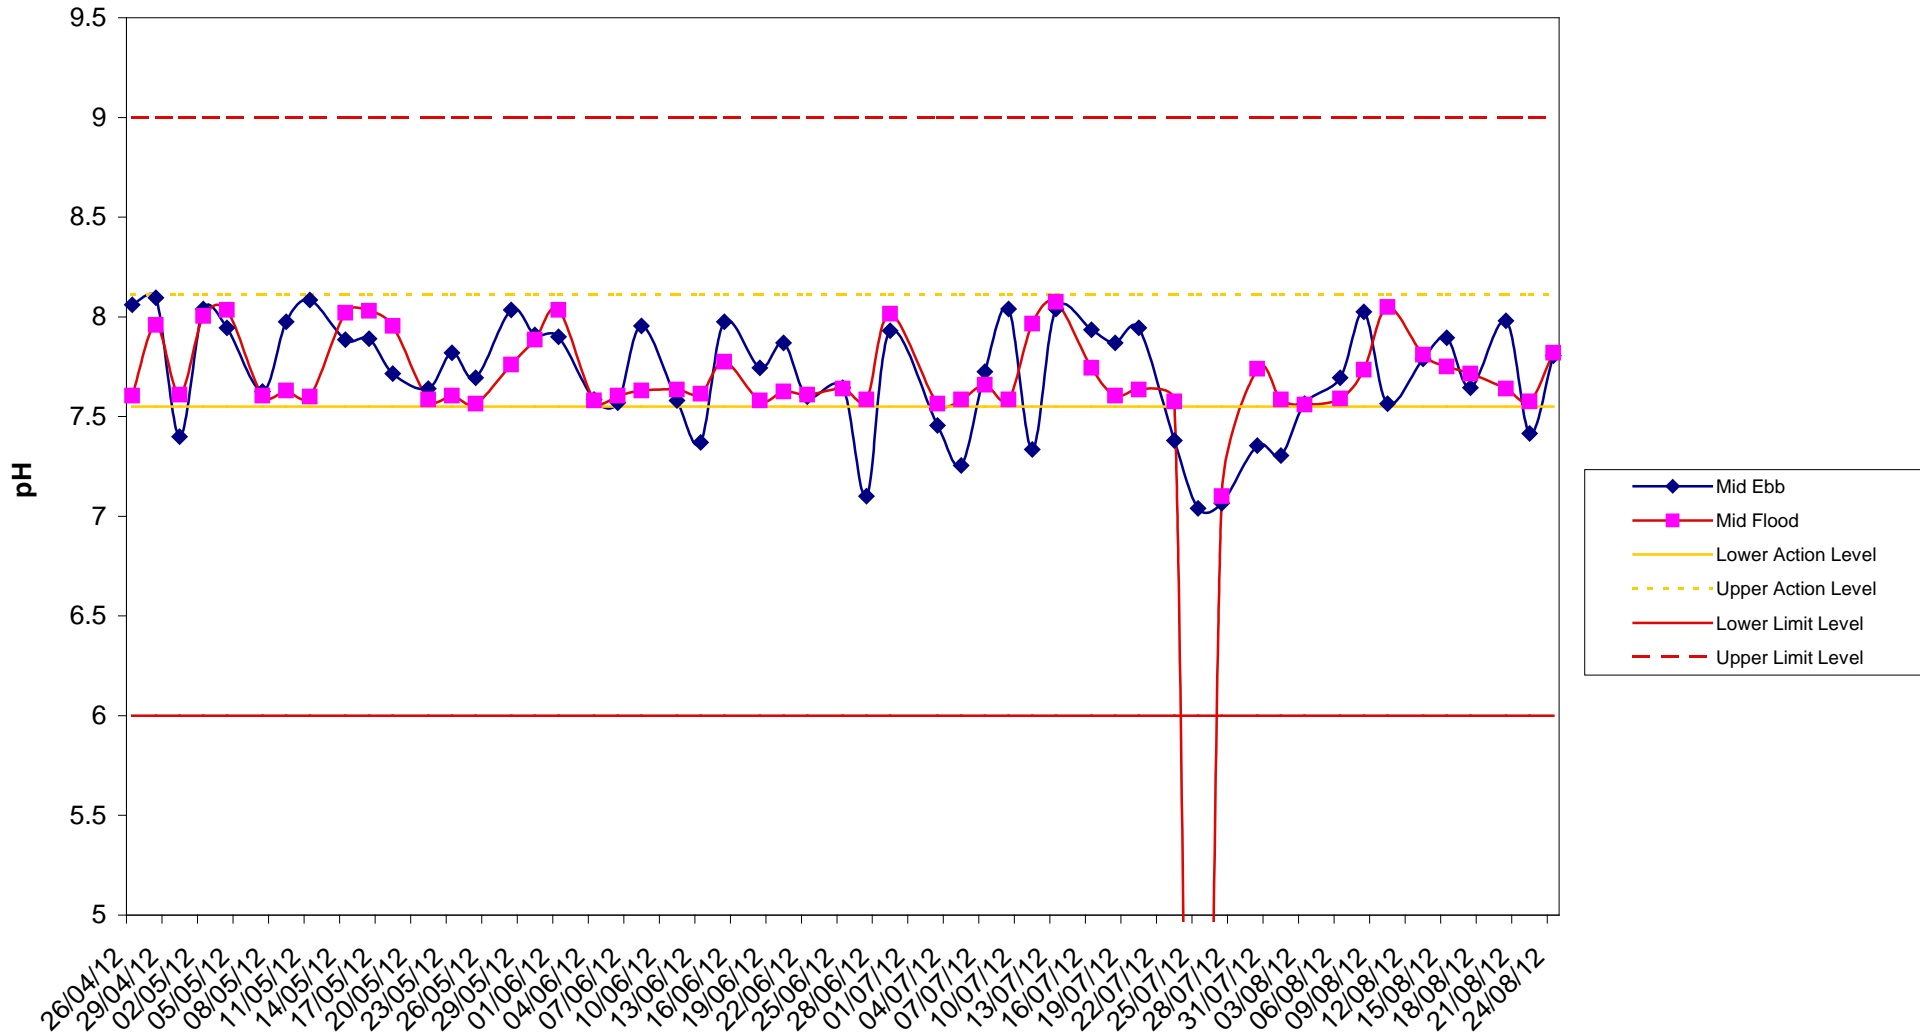


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - Suspended Solids Content (Mid-Ebb)

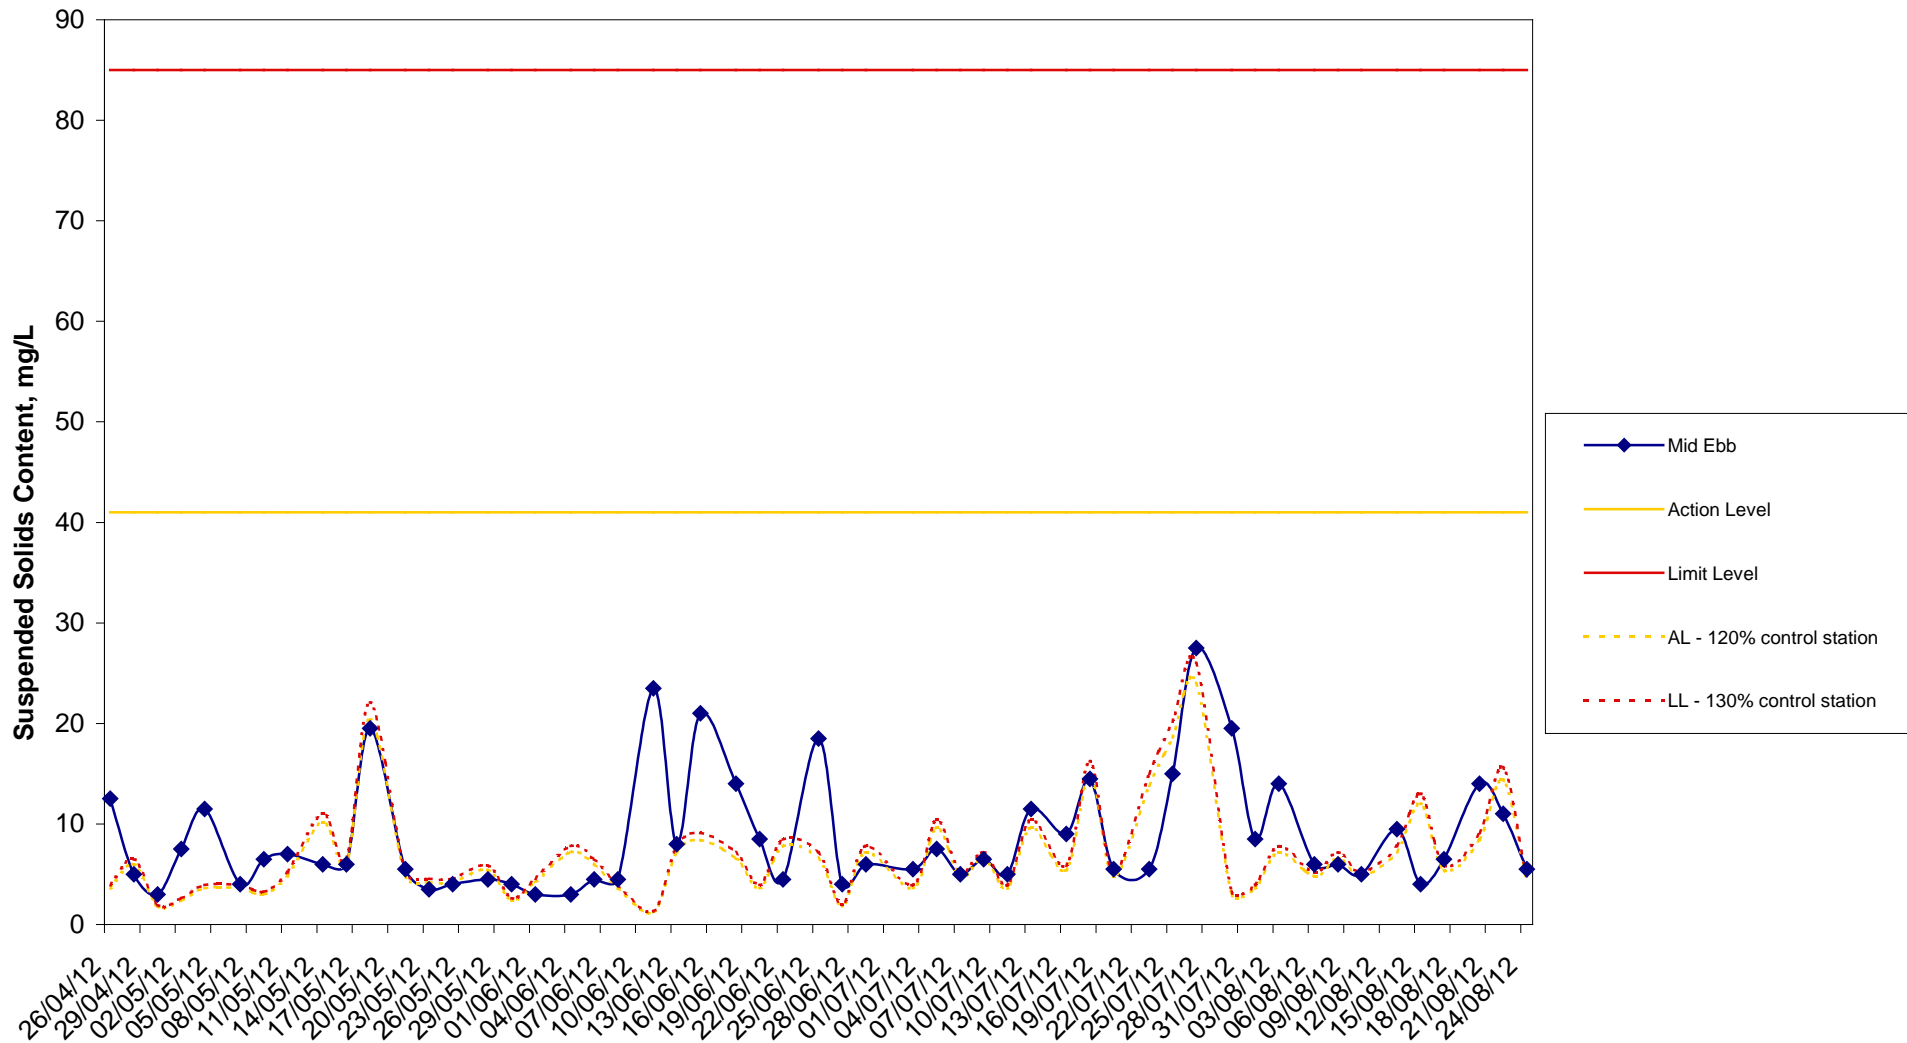


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



W3 - Suspended Solids Content (Mid-Flood)

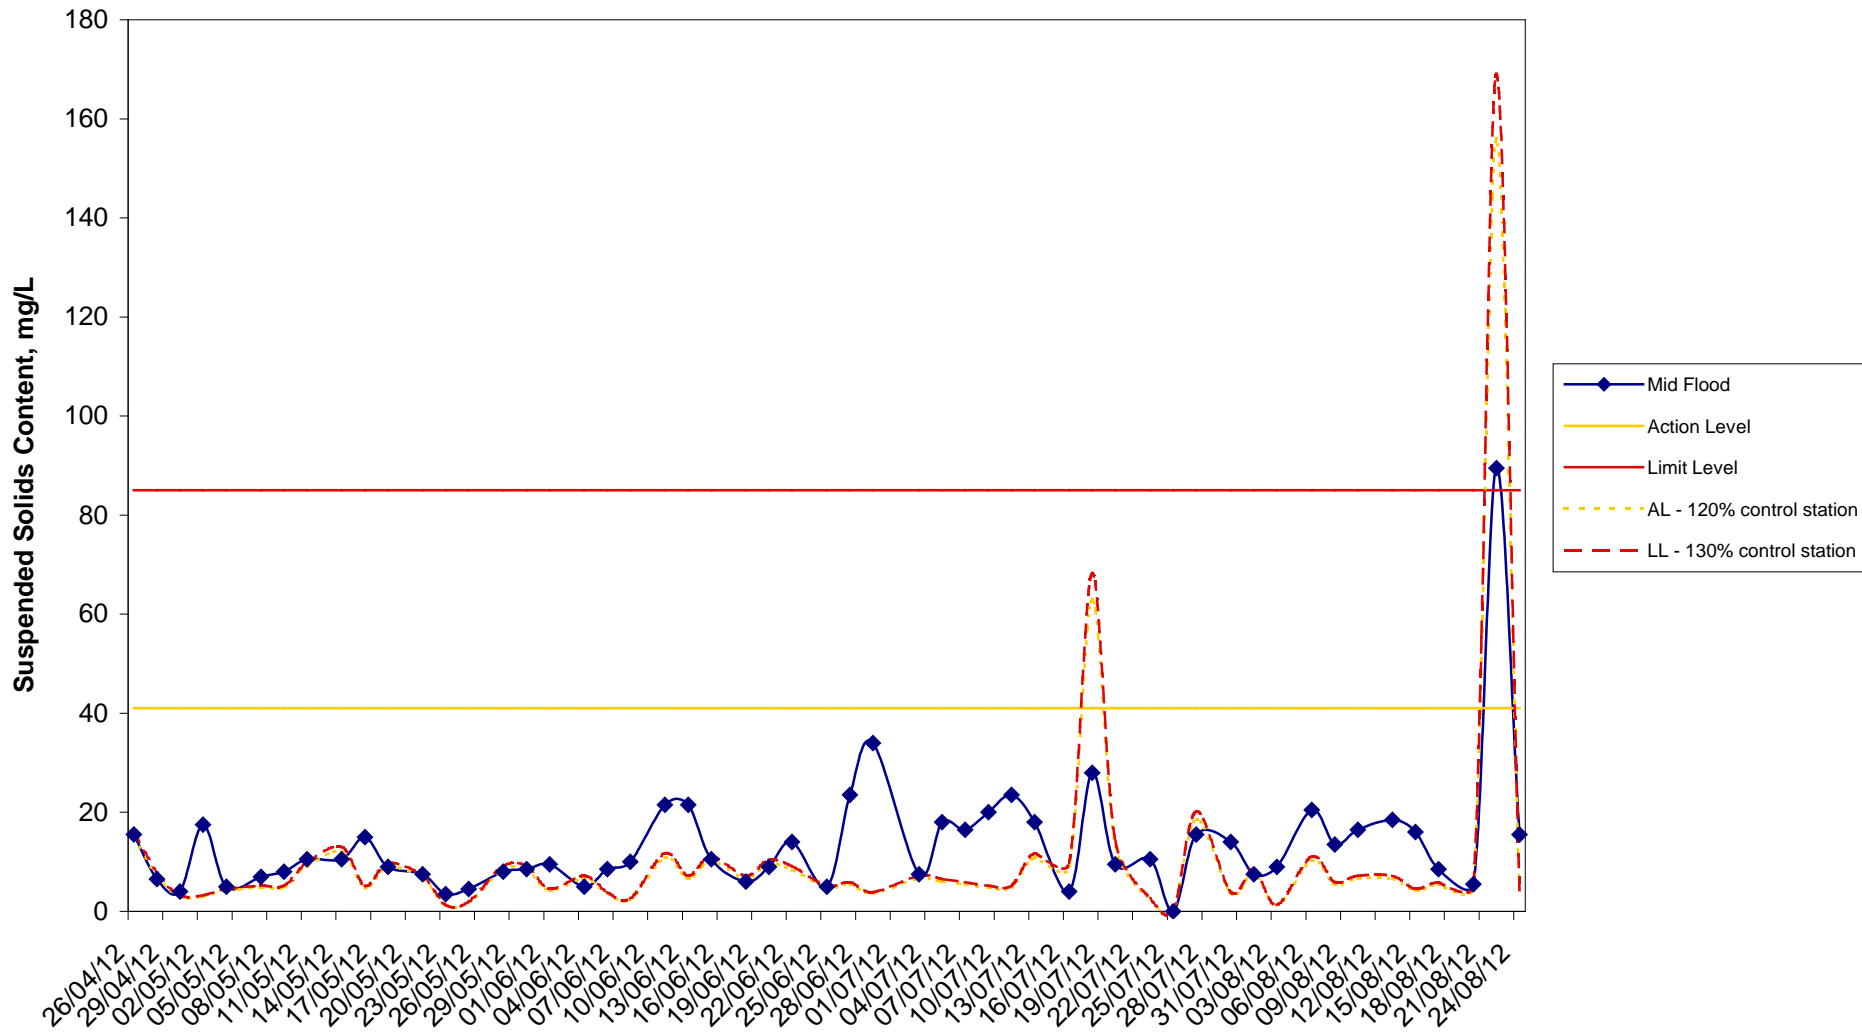


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Dissolved Oxygen Content

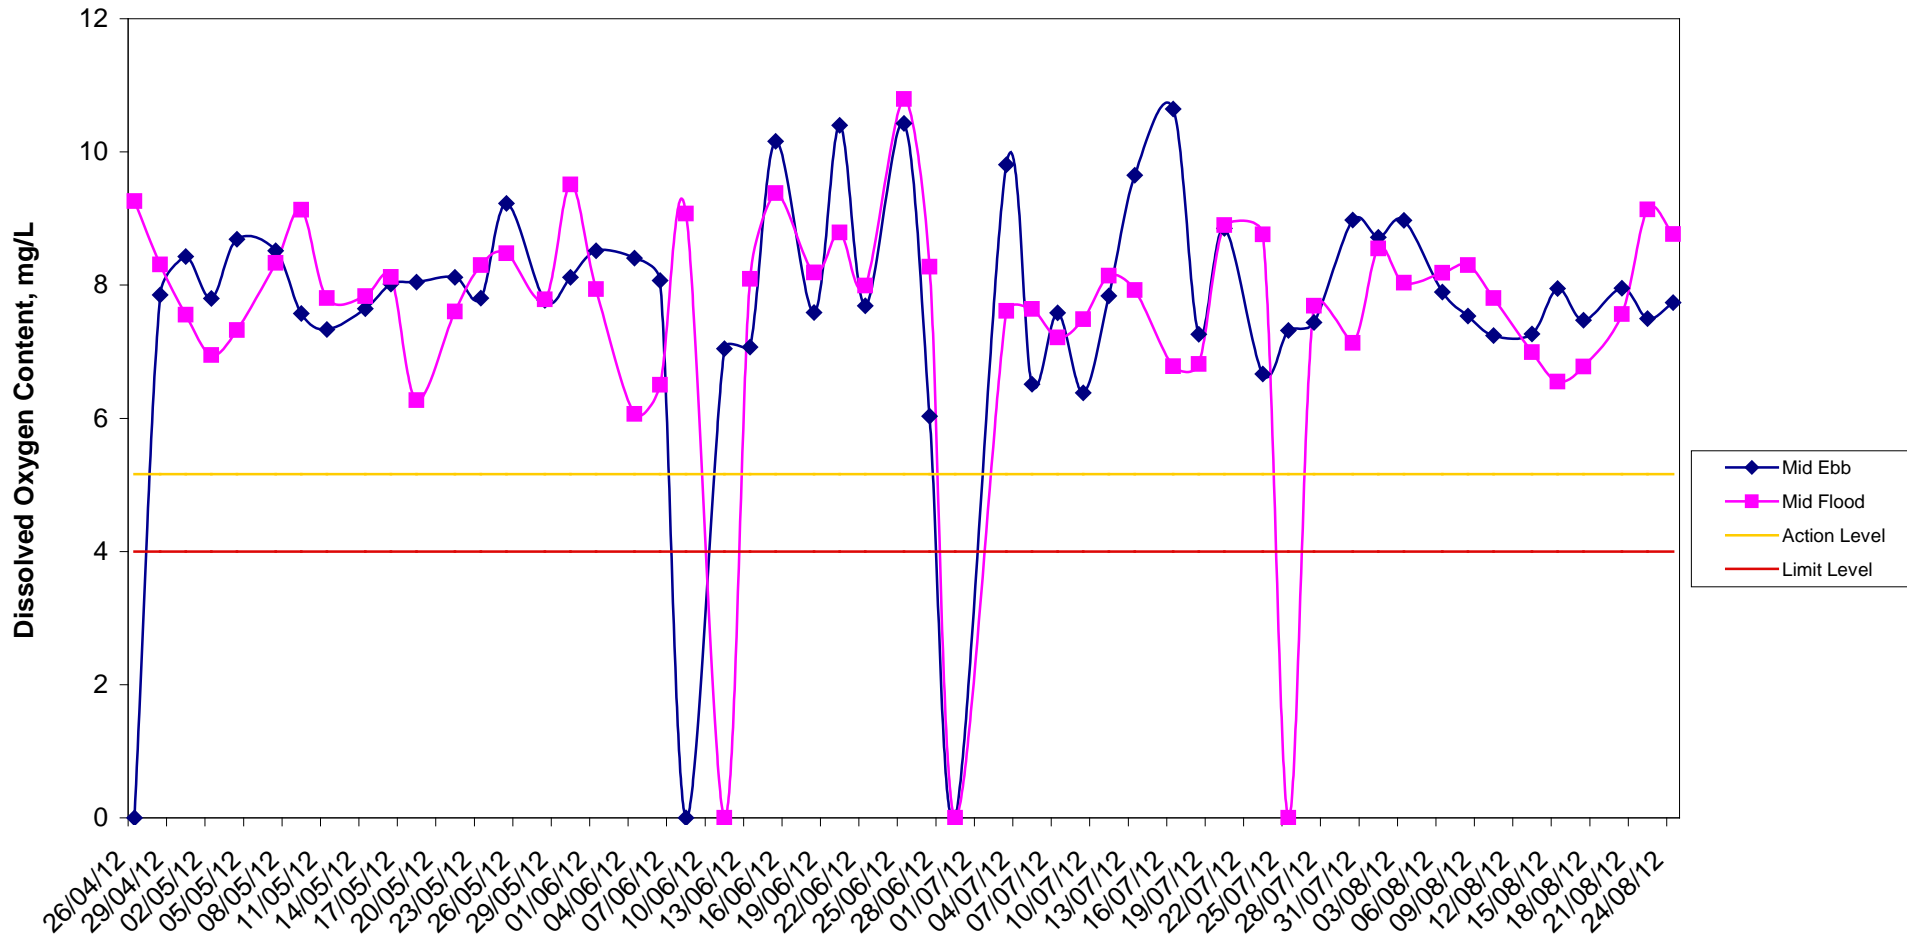

Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Turbidity

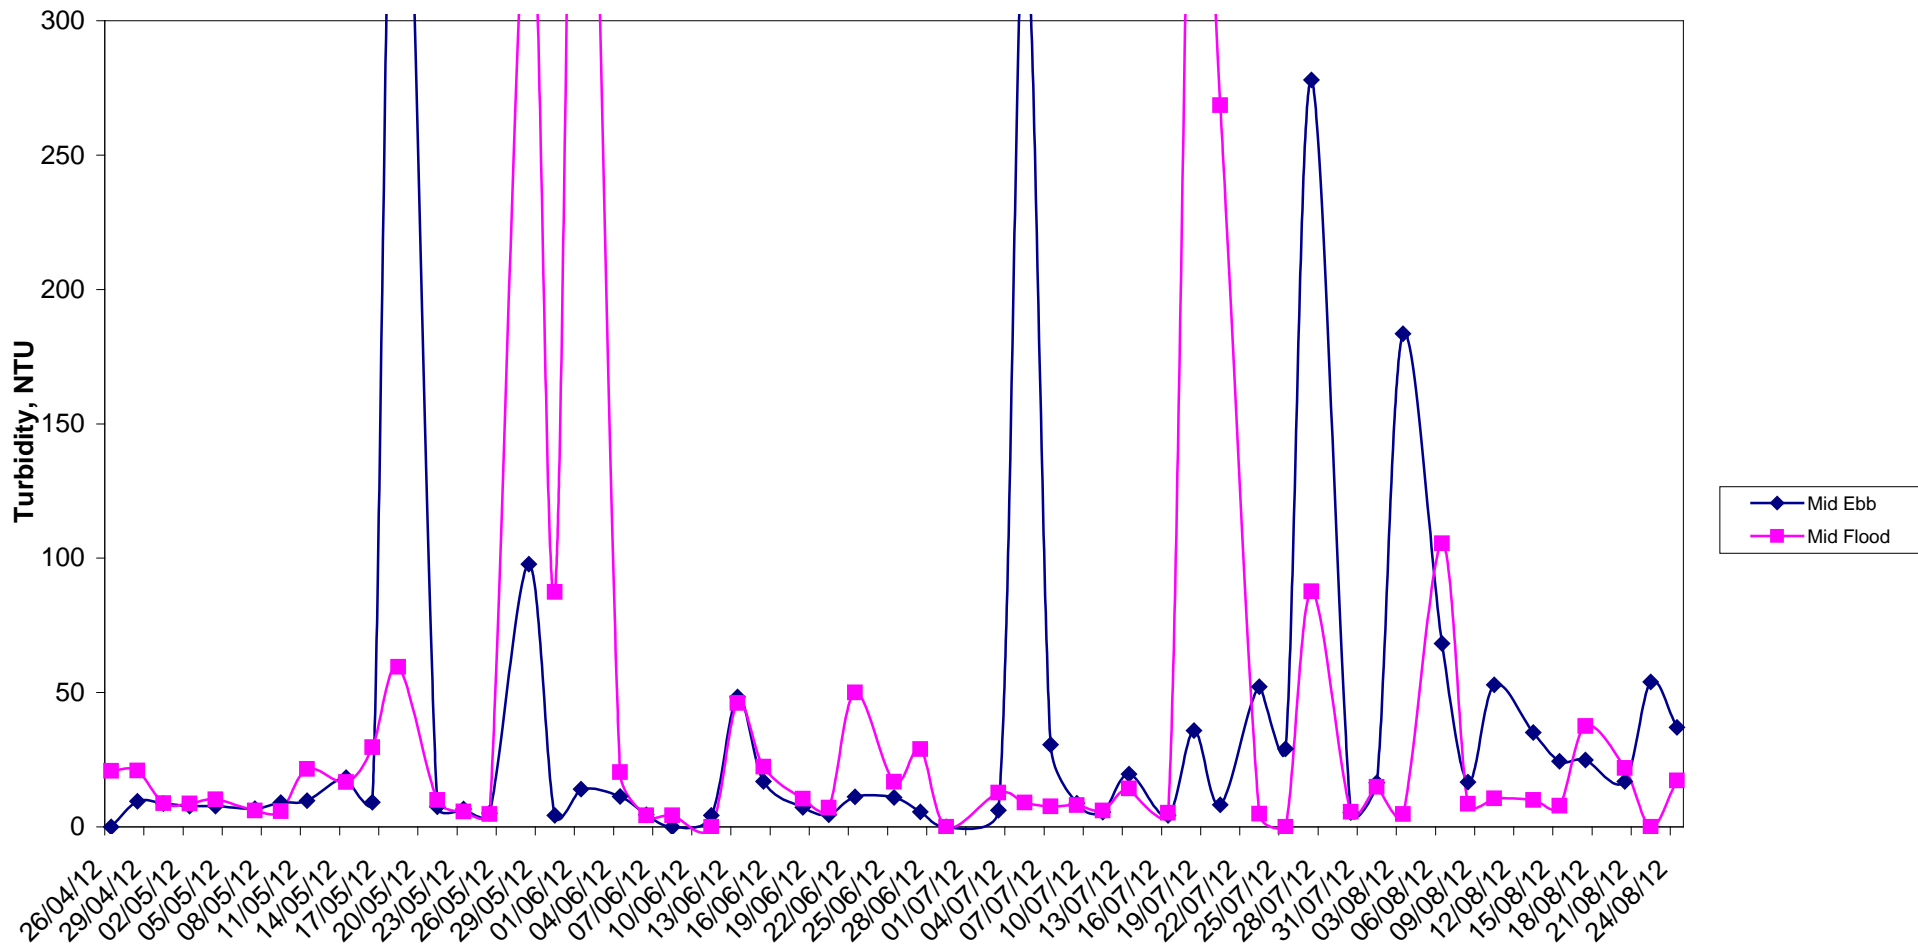

Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - pH

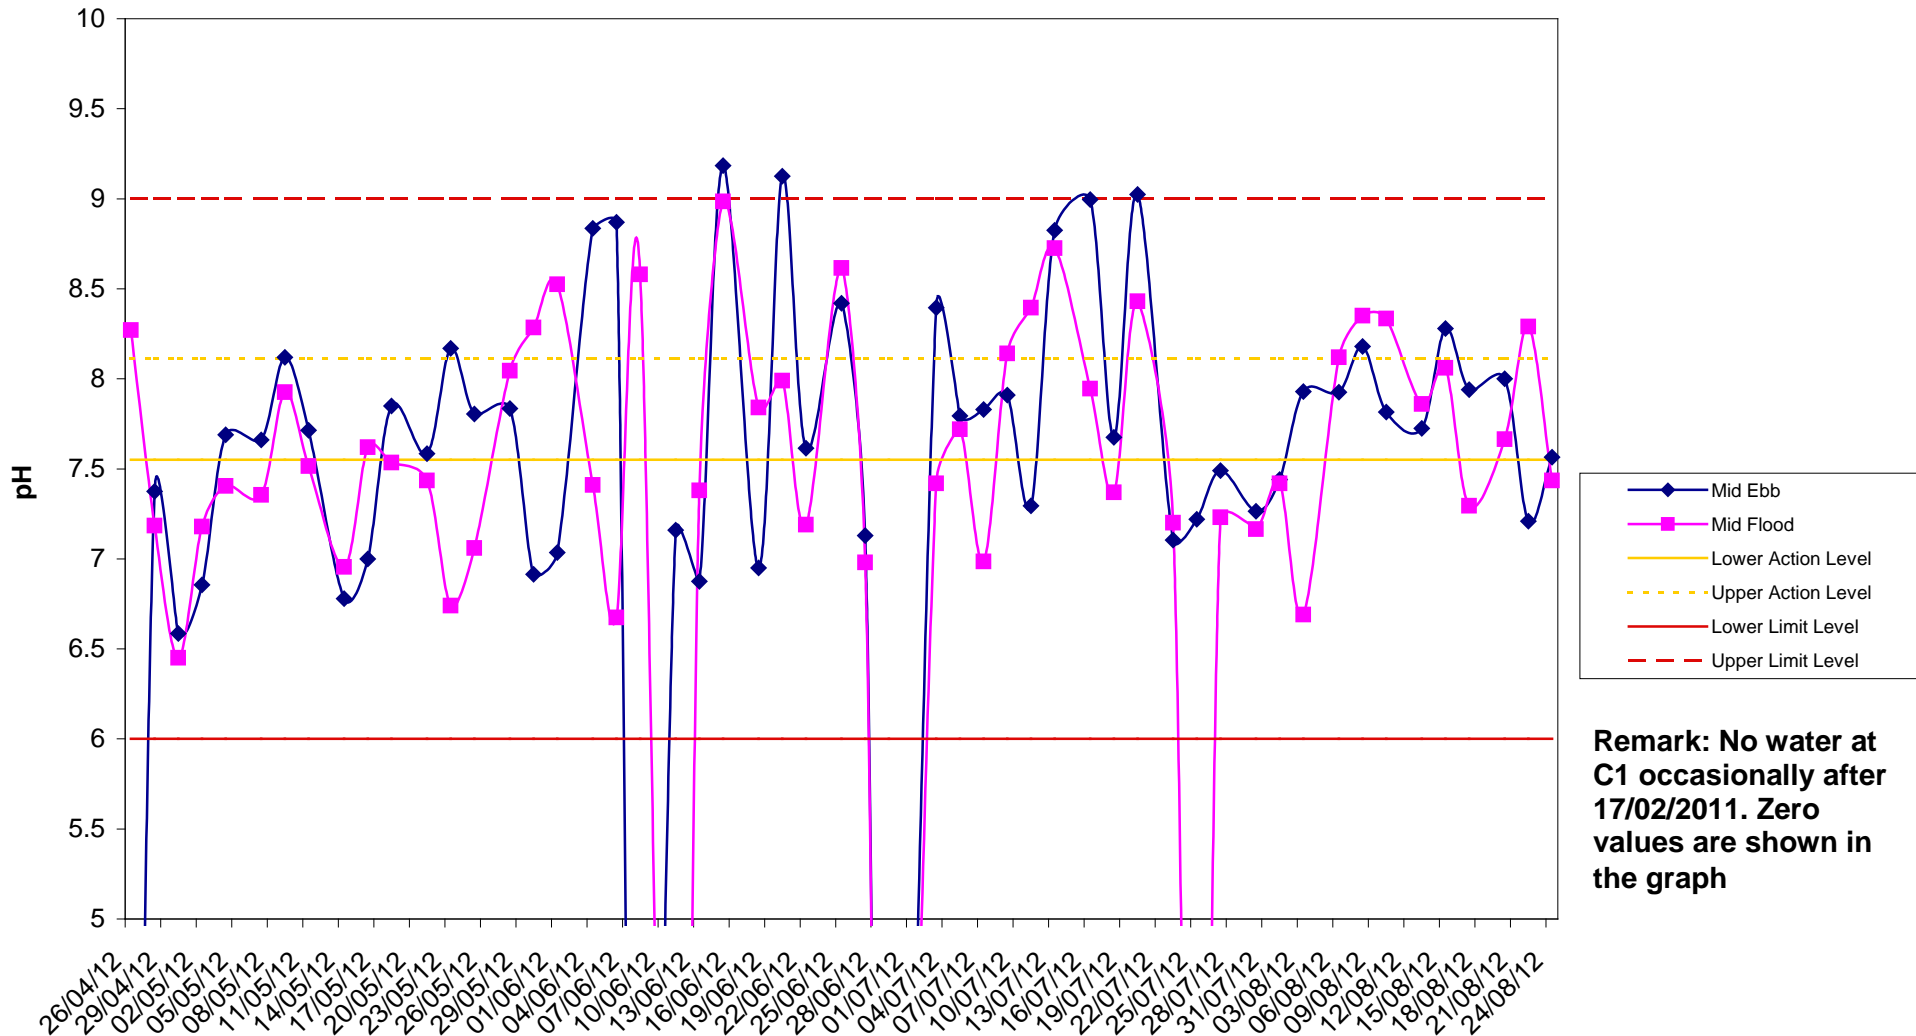

Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Suspended Solids Content

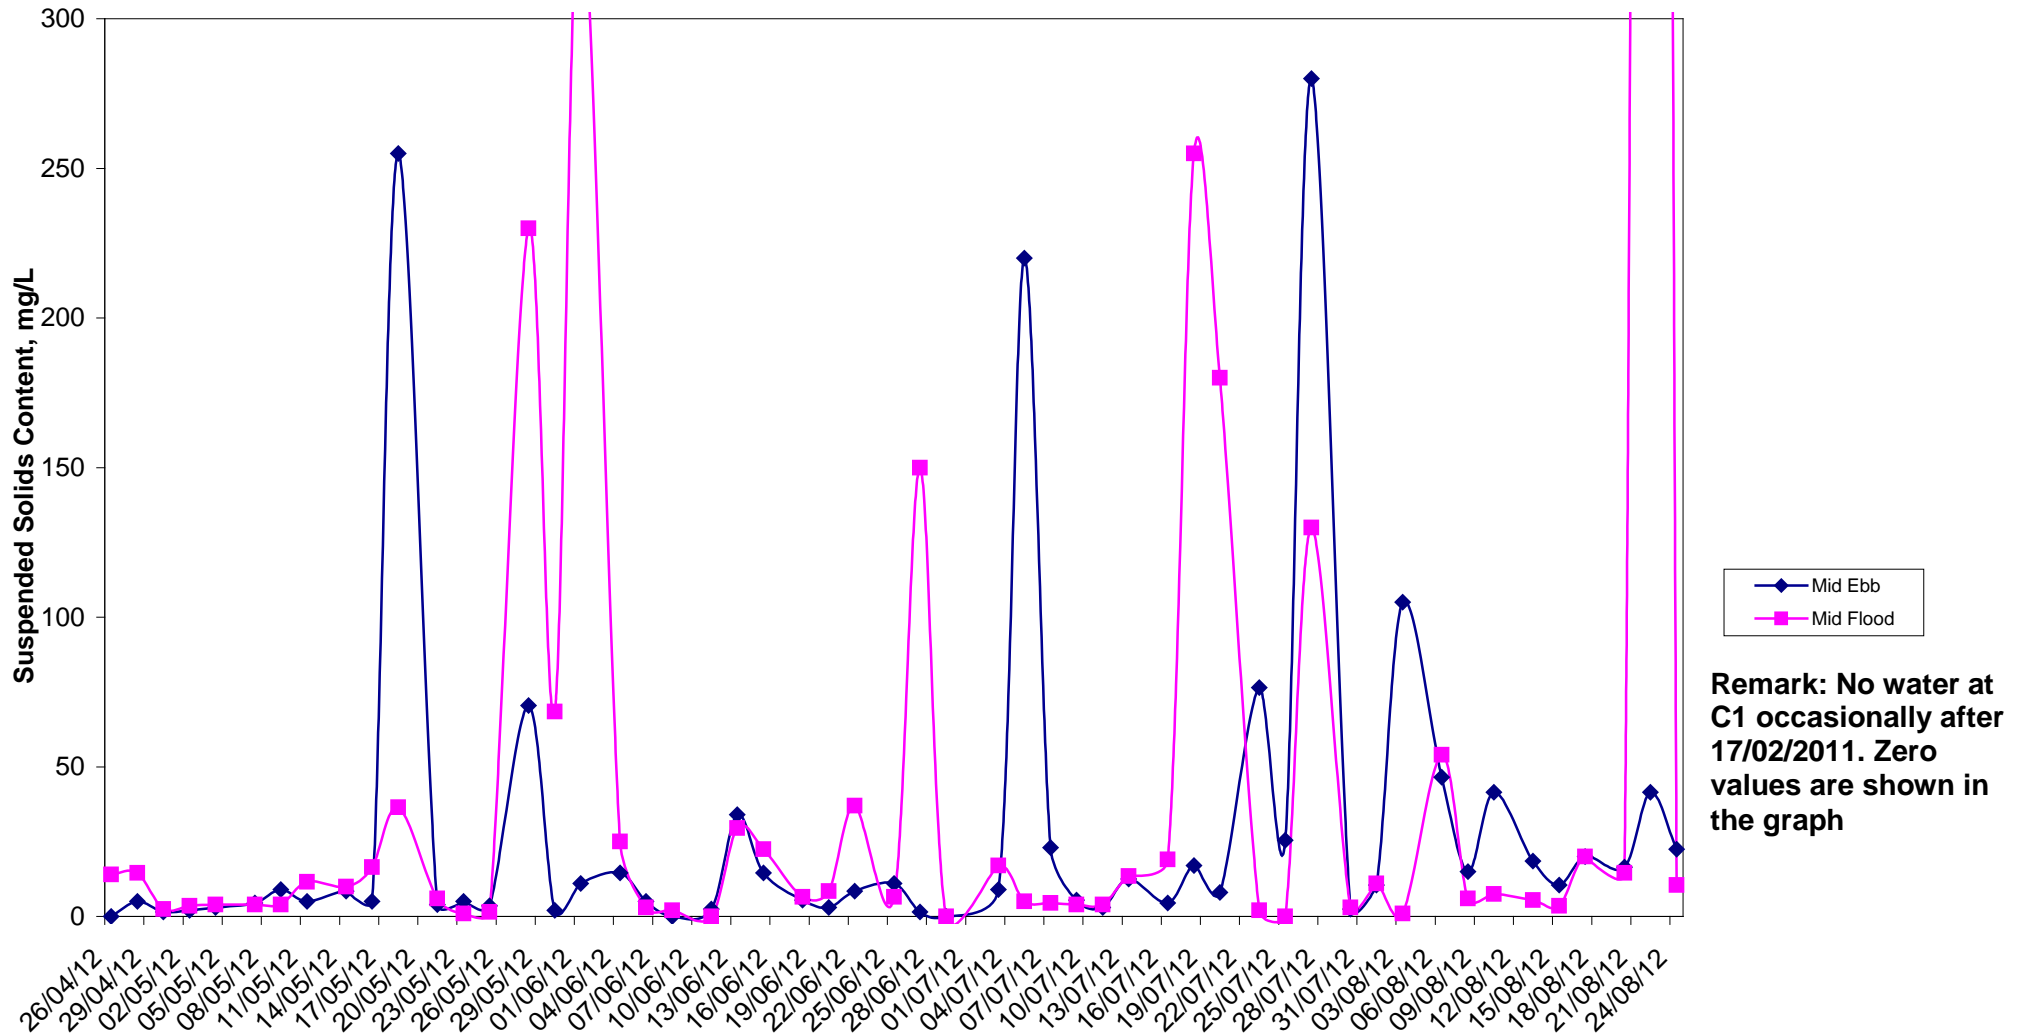


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C2 - Dissolved Oxygen Content

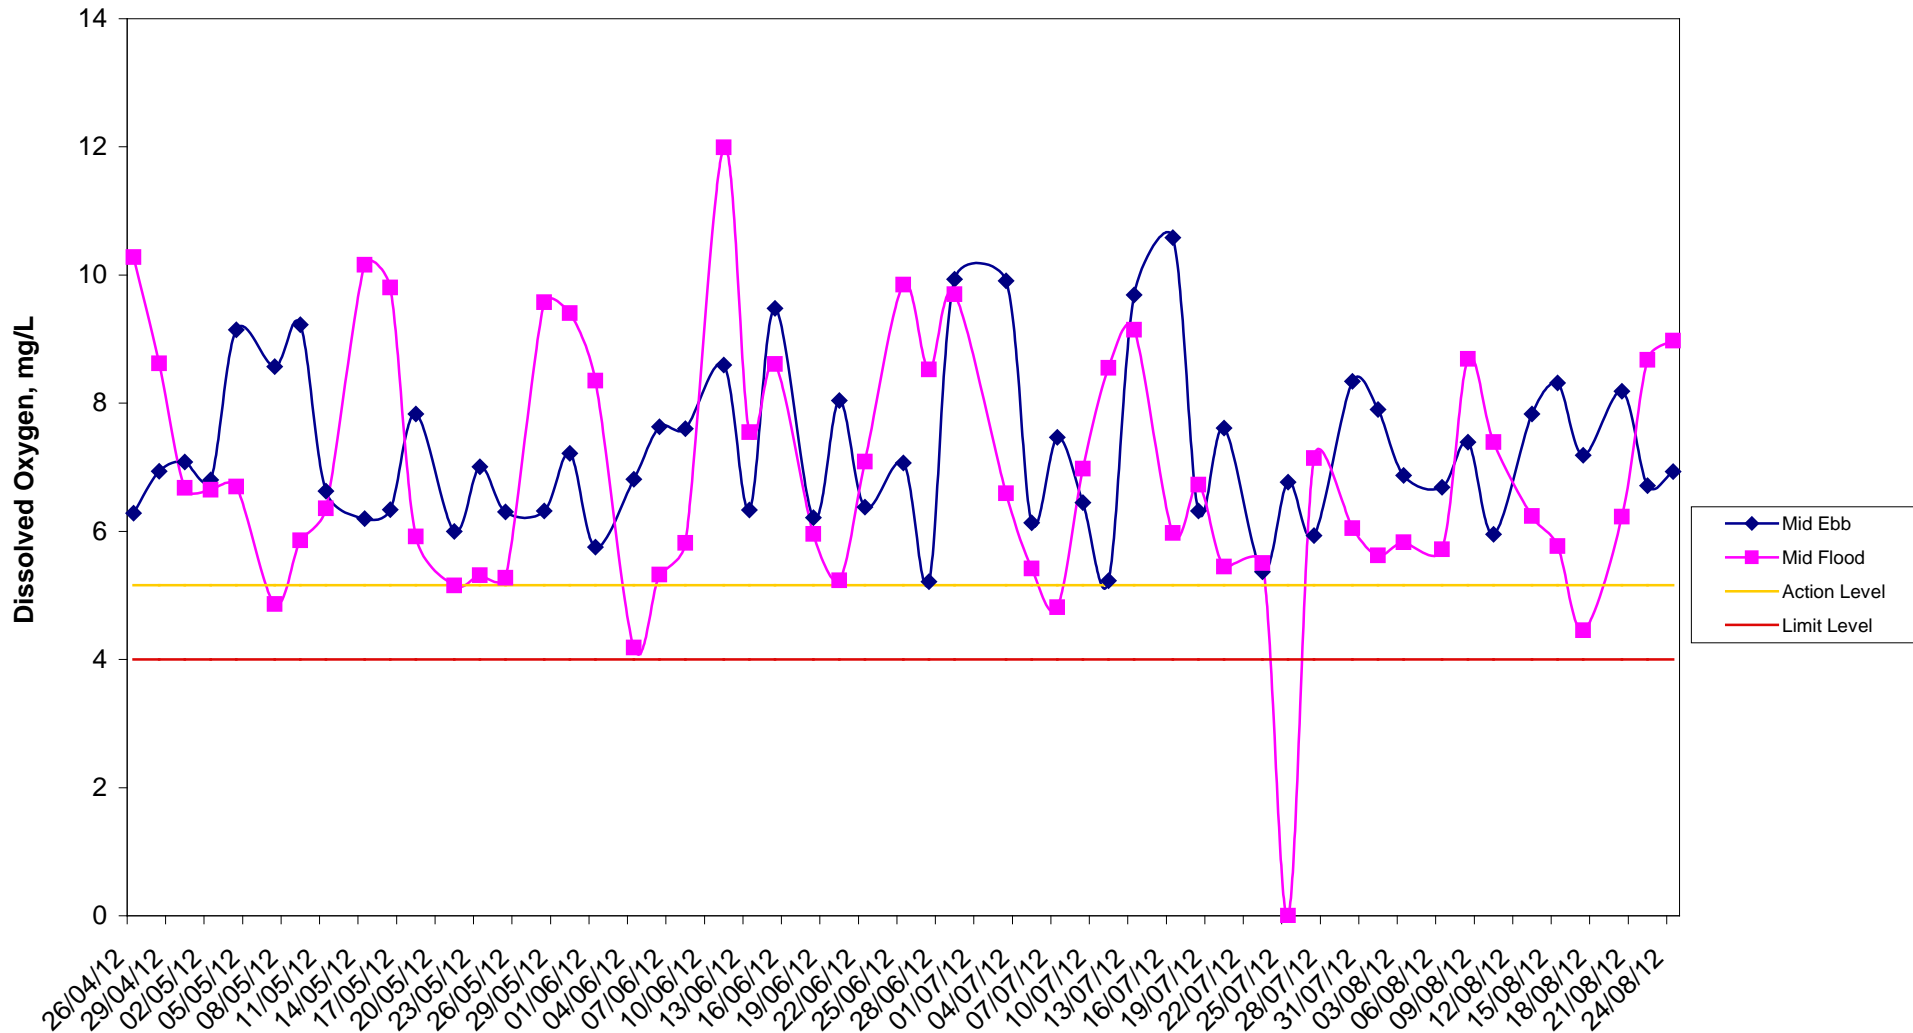


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C2 - Turbidity

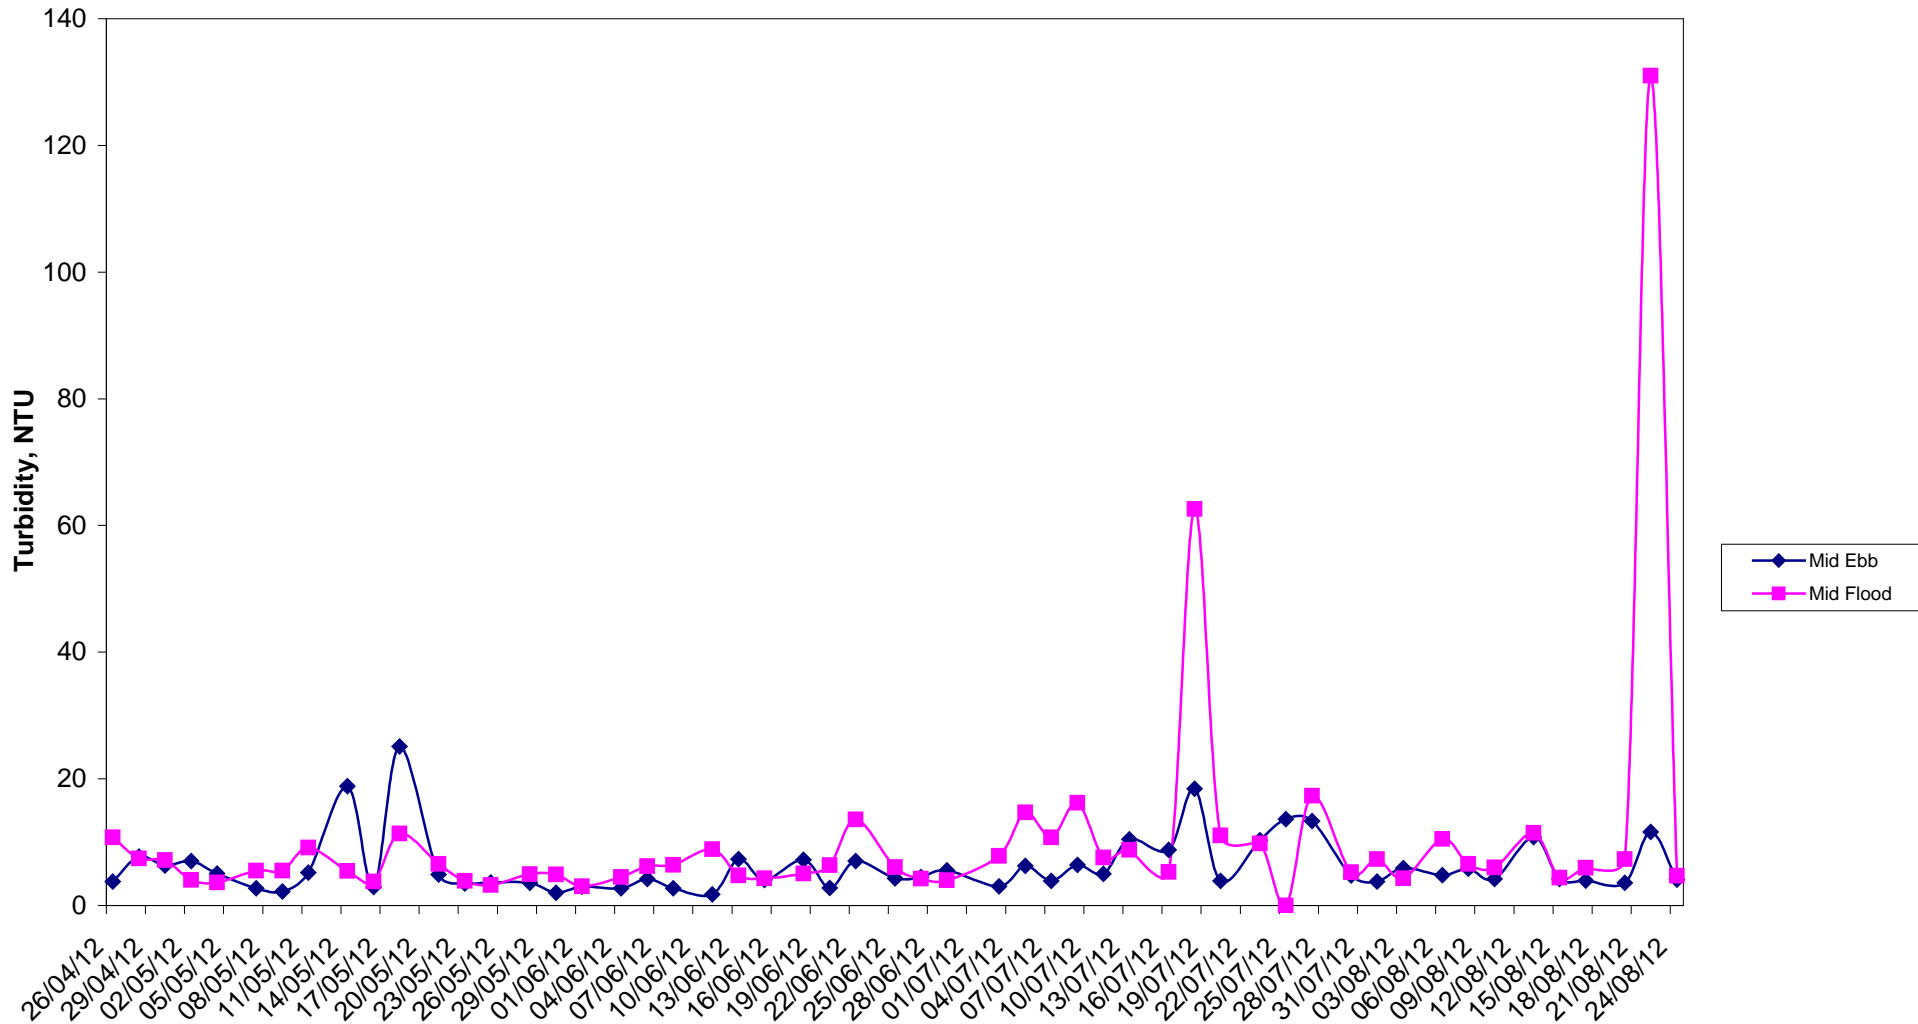


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C2 - pH

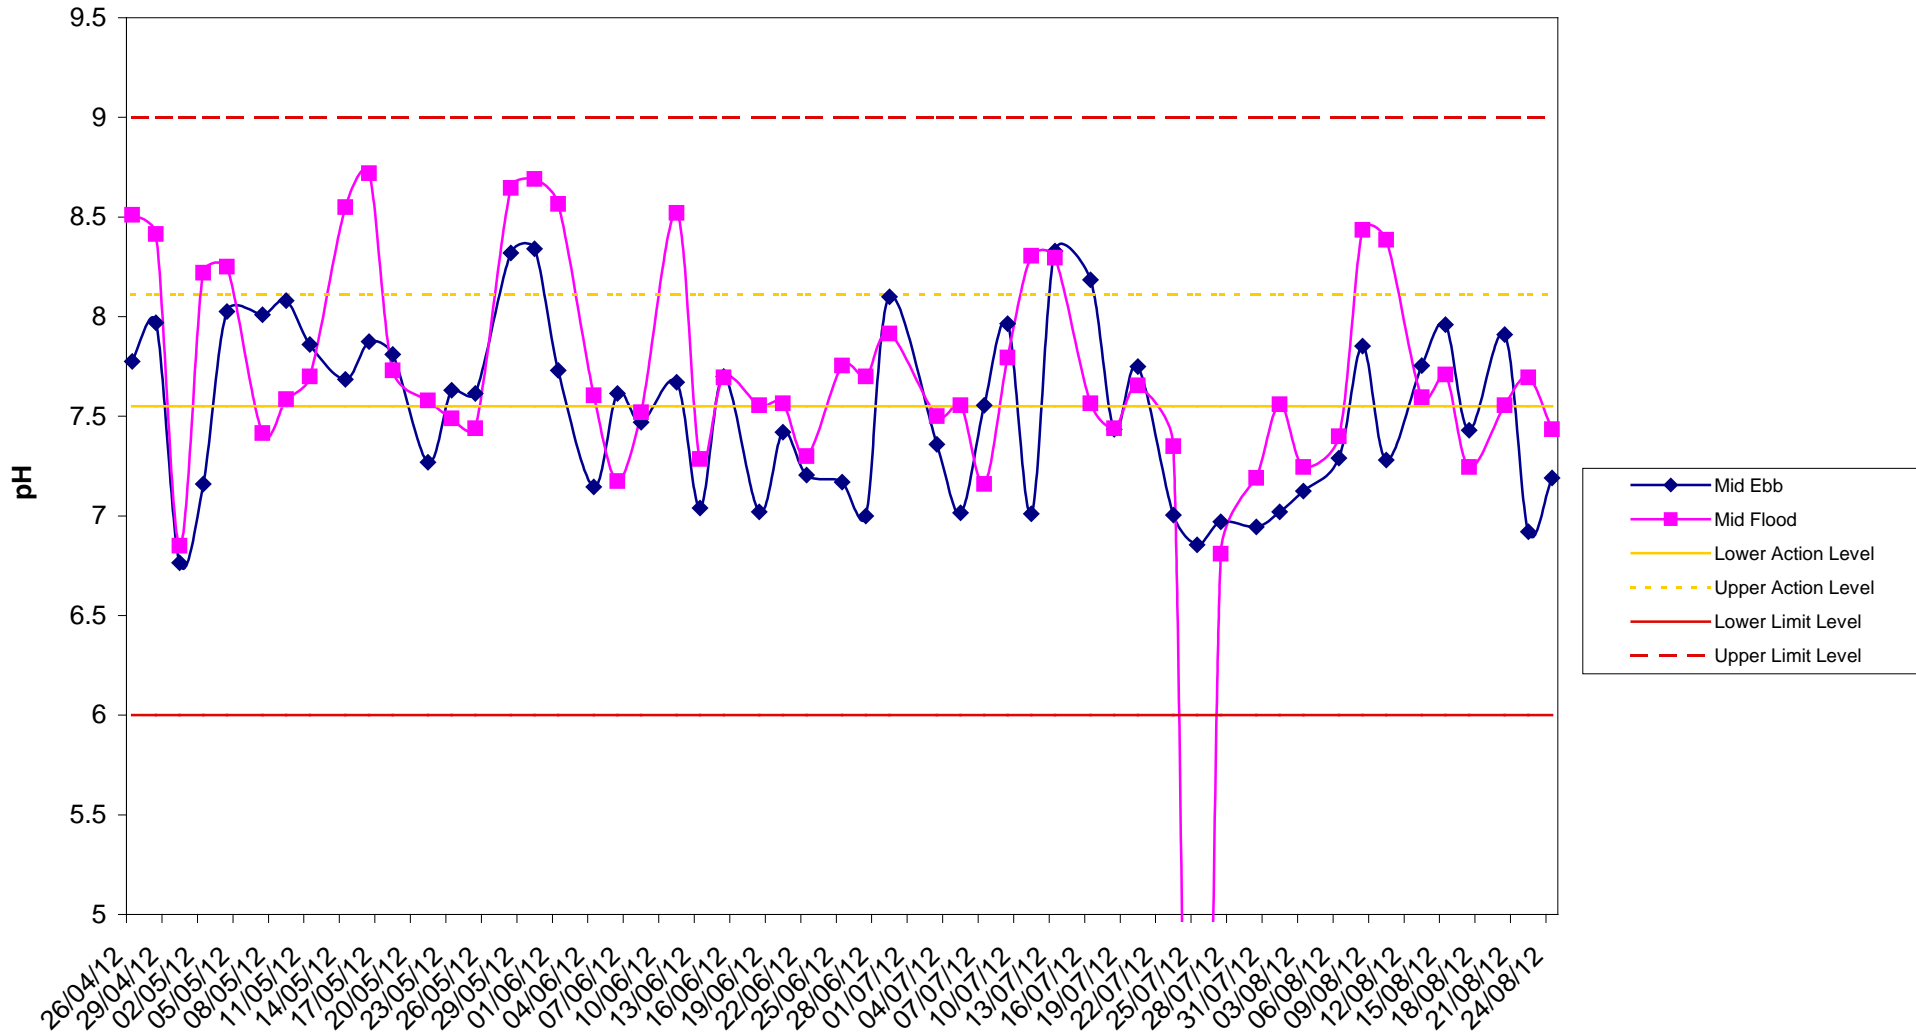


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C2 - Suspended Solids Content

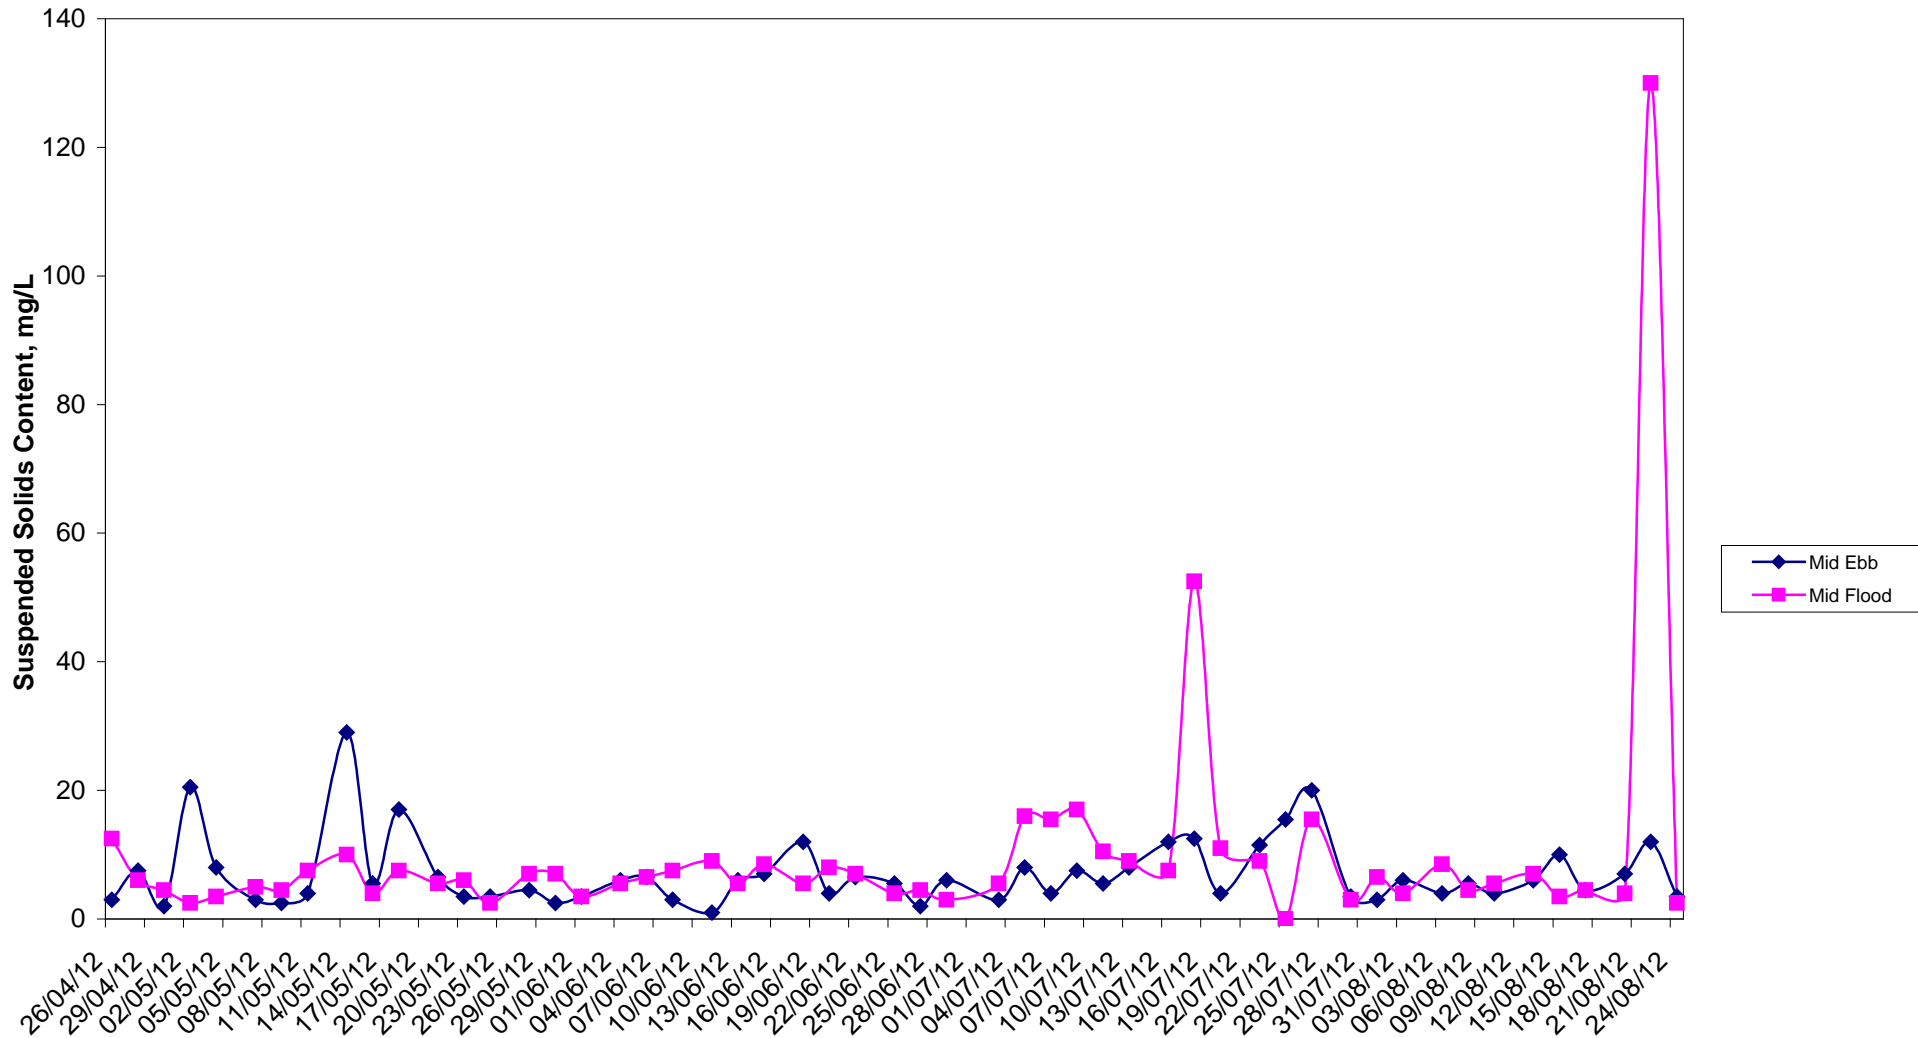


FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MaterialLab

M1 - Aluminium Content

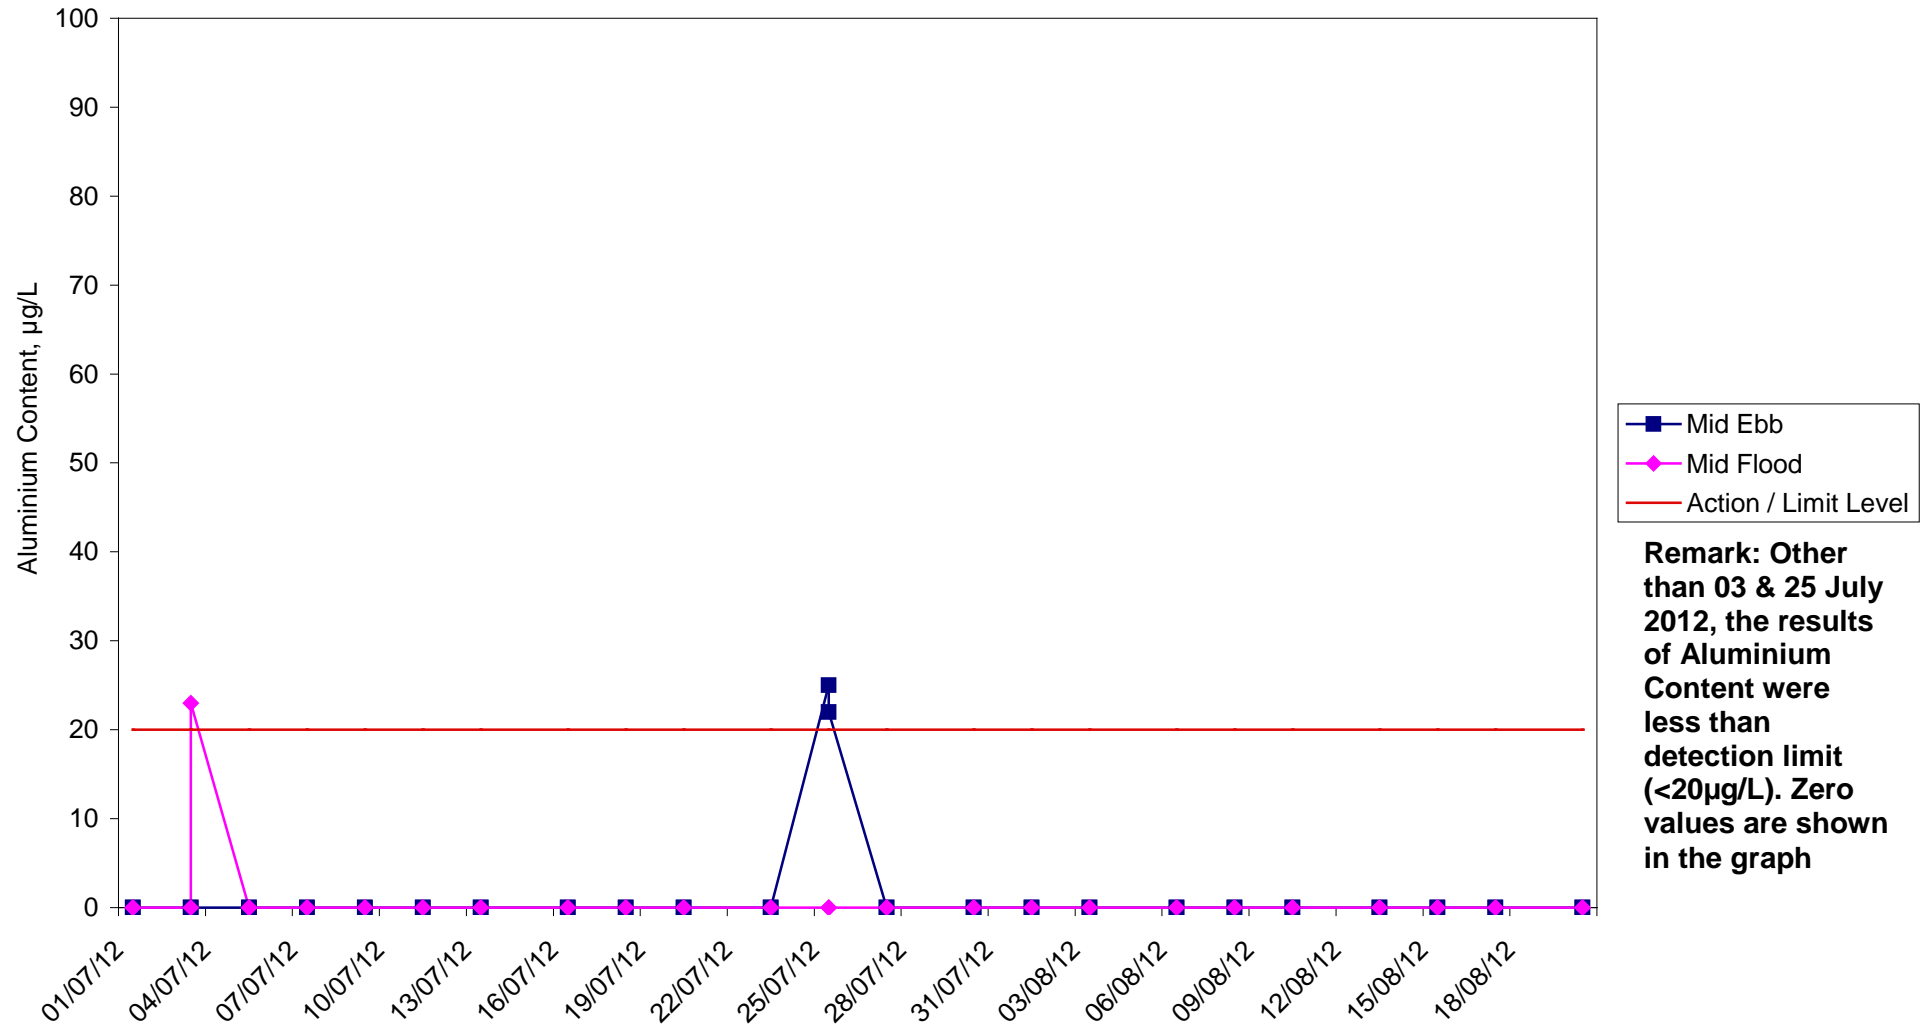

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 5 Construction Program

HONG KONG SLUDGE TREATMENT FACILITY Project Overview

Date 02DEC10	Revision VLJH-WT-ZZ-0002-D01	Checked RGU	Approved NFR
-----------------	---------------------------------	----------------	-----------------

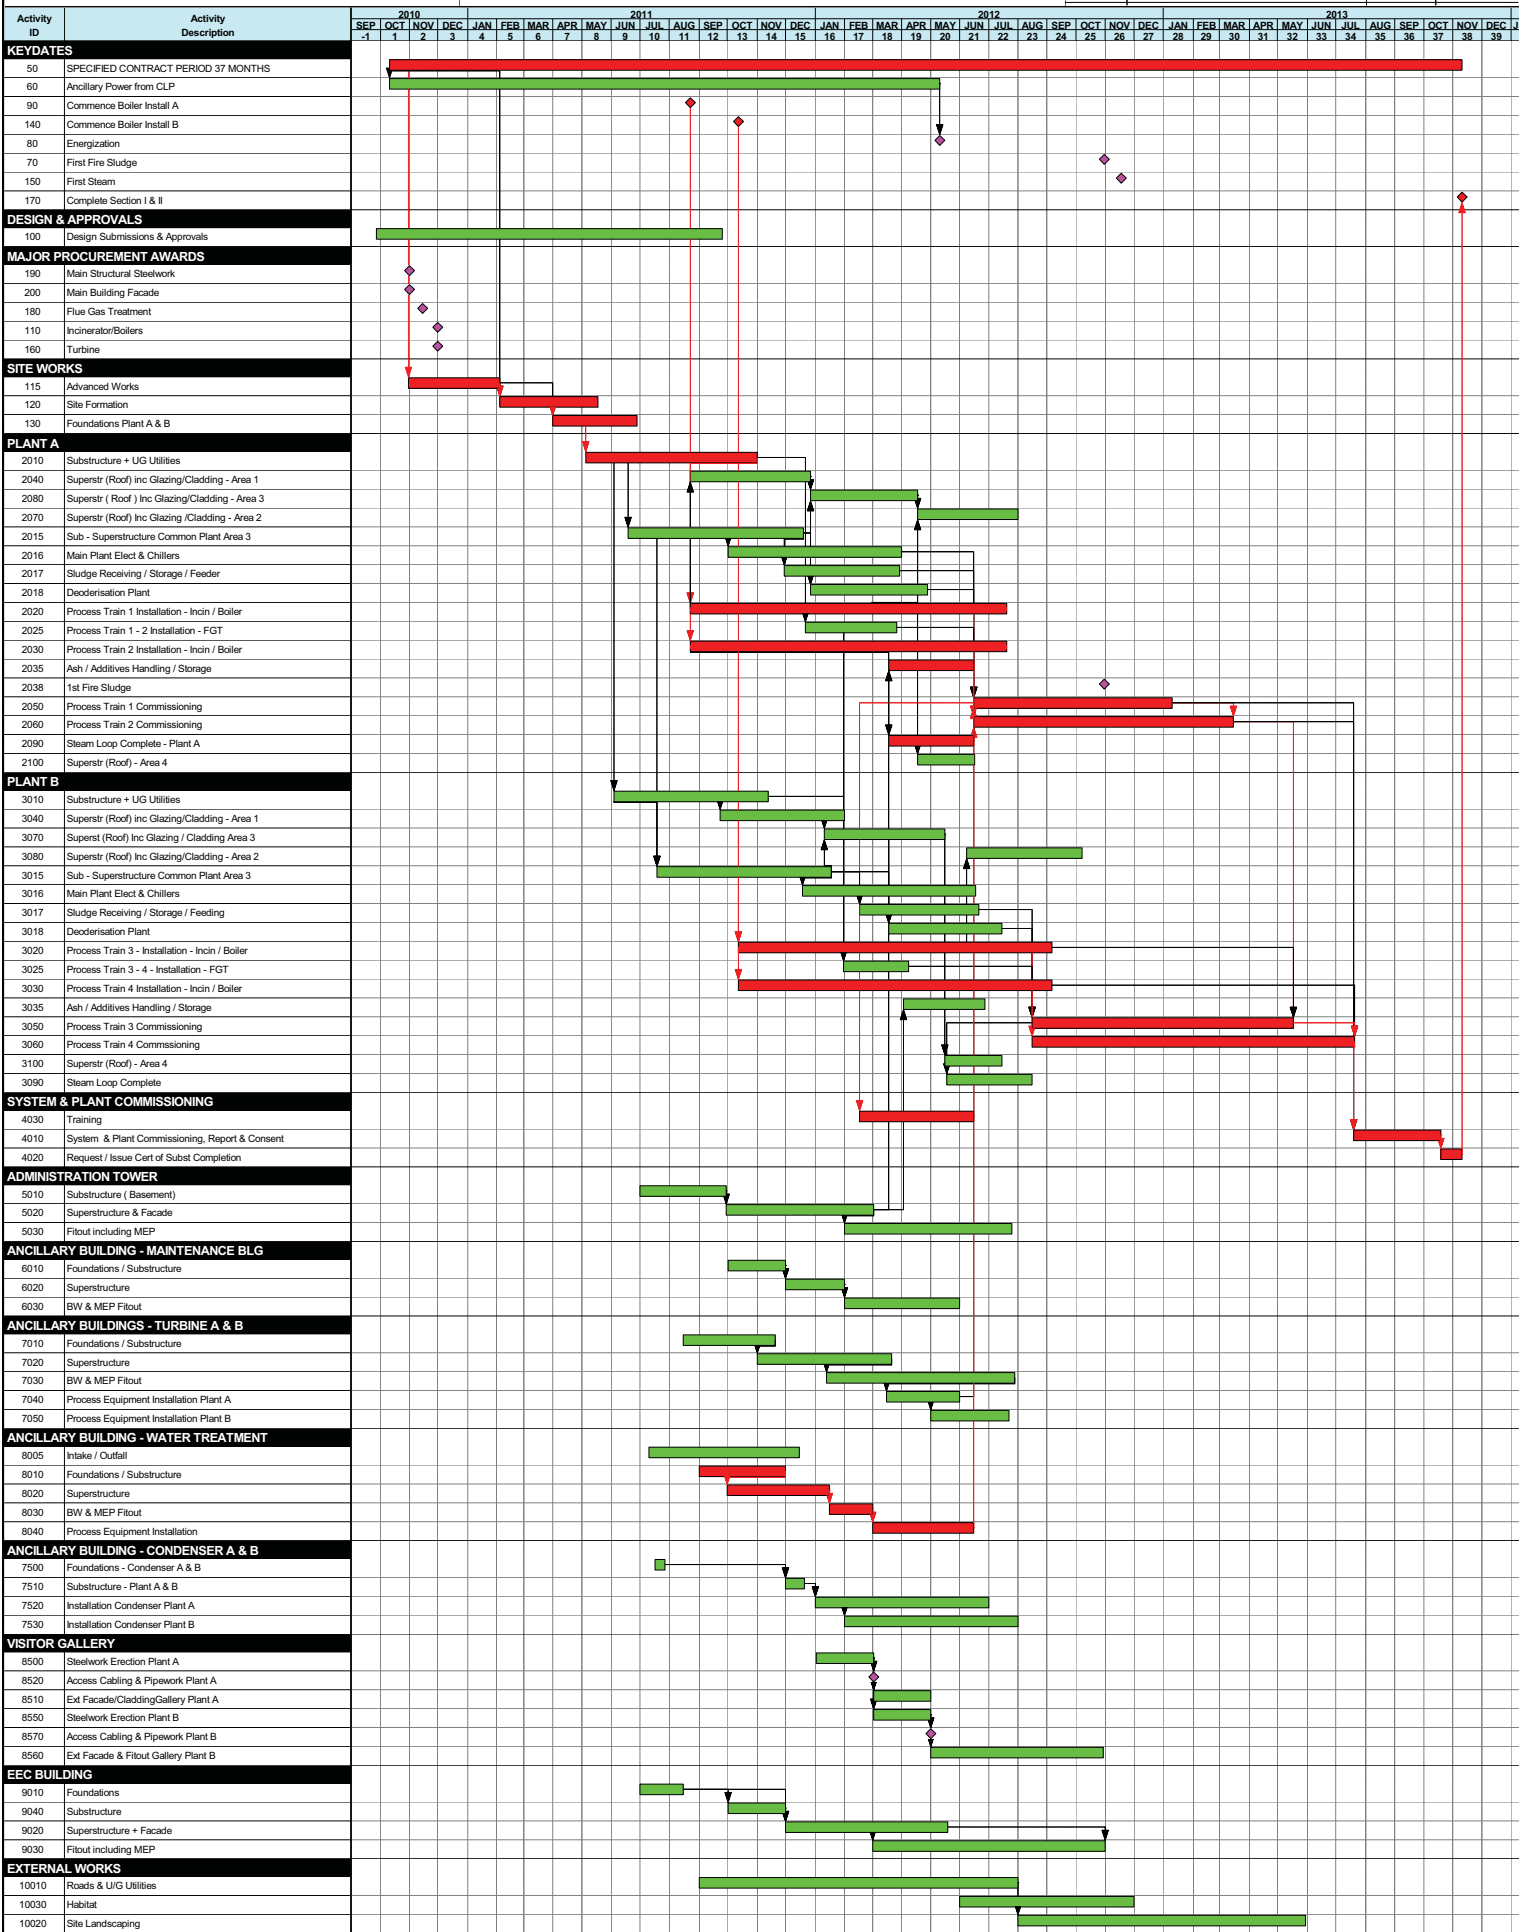

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 6

Management Structure and Organization Chart


FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materialab.com.hk



Management Structure and Organization Chart

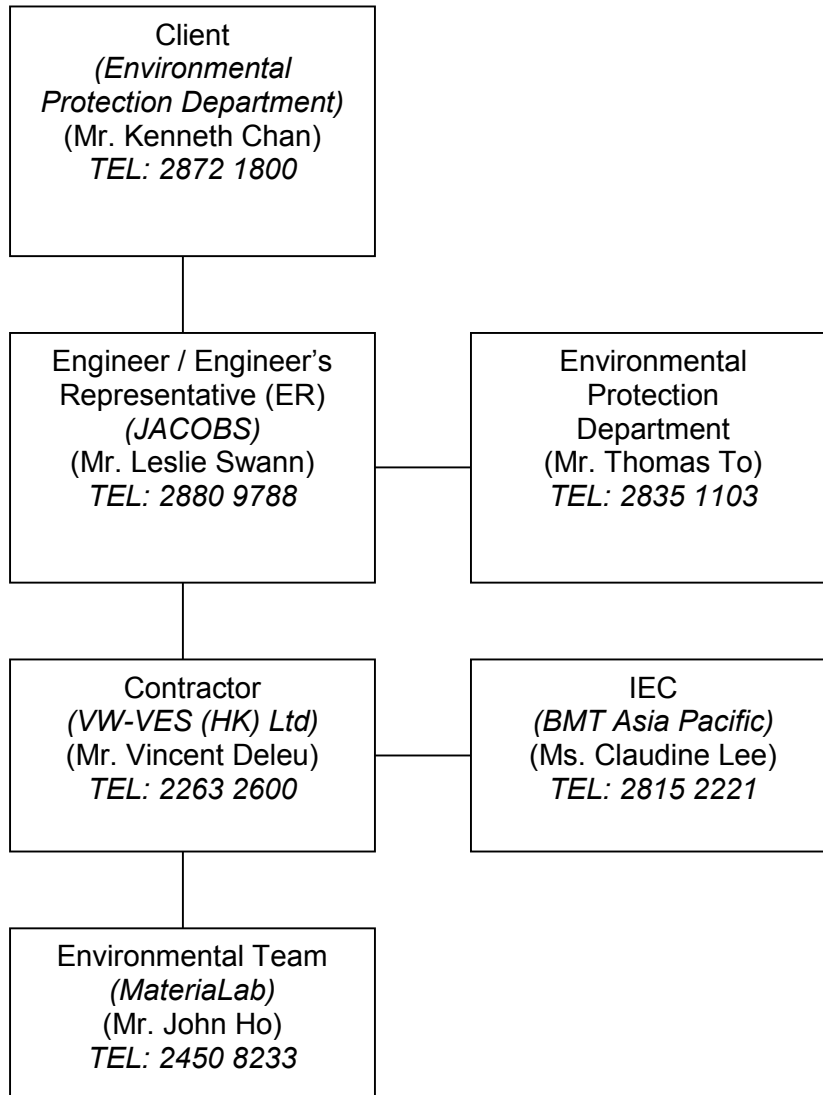

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 7

Event / Action Plan for Water Quality

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Event/Action Plan for Water Quality

Event	ET Leader	IEC	SOR	Contractor
Action level being exceeded by one sampling day	<ul style="list-style-type: none"> Repeat <i>in situ</i> measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance. 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SOR; Implement the agreed mitigation measures.
Action level being exceeded by more than one consecutive sampling day	<ul style="list-style-type: none"> Repeat <i>in situ</i> measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC on the Proposed mitigation measures; Make agreement on the mitigation measures to be implemented; ◆ Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SOR within three working days; Implement the agreed mitigation measures.

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



	<ul style="list-style-type: none"> increase the monitoring frequency to daily; Repeat measurement on next day of exceedance. 			
Limit level being exceeded by one sampling day	<ul style="list-style-type: none"> Repeat <i>in situ</i> measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, SOR and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days; Implement the agreed mitigation measures.
Limit level being exceeded by more than one consecutive sampling day	<ul style="list-style-type: none"> Repeat <i>in situ</i> measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness 	<ul style="list-style-type: none"> Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and SOR and

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
 Fugro Development Centre,
 5 Lok Yi Street, 17 M.S. Castle Peak Road,
 Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
 Telefax : +852-2450 6138
 E-mail : matlab@fugro.com.hk
 Website : www.fugro.com



	<ul style="list-style-type: none"> • Discuss mitigation measures with IEC, SOR and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. 		<p>of the implemented mitigation measures;</p> <ul style="list-style-type: none"> • Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level. 	<p>propose mitigation measures to IEC and SOR within three working days;</p> <ul style="list-style-type: none"> • Implement the agreed mitigation measures; • As directed by the SOR, to slow down or to stop all or part of the construction activities.
--	---	--	---	---

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 8

Implementation Schedule of Mitigation Measures

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


Table 1. Implementation Schedule and Status of Proposed Air Quality Mitigation Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.8.1	<p>Implementation of the Air Pollution Control (Construction Dust) Regulation and good site practices:</p> <ul style="list-style-type: none"> • Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. • Use of frequent watering for particularly dusty construction areas and areas close to ASRs. • Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines. • Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. • Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. • Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. • Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. 	Work site / During the construction period	Contractor		√			Air Pollution Control (Construction Dust) Regulation

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit. Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs. Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. 				√			
					√			
					√			

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



Table 2. Implementation Schedule of Proposed Human Health Risk Mitigation Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Human Health Risk Associated with Radon</u></p> <p><i>Prevention of radon influx from the PFA to the STF buildings</i></p> <ul style="list-style-type: none"> A soil cover can be provided beneath the buildings on top of ash lagoon prior to construction works because it reduces the level of radon influx significantly Slab-on-grade can be an option on foundation design Soil suction can also prevent radon from entering the building by drawing the radon from below the building and venting it through a pipe, or pipes, to the air above the building. <p><i>Provision of Sufficient ventilation of the interior of the STF buildings</i></p> <ul style="list-style-type: none"> Forced and natural ventilation should be introduced properly to enhance air exchange rate in the STF buildings. Basement areas should be pressurized by using a fan to blow air into the basement areas from outdoors is suggested. This would create enough pressure at the lowest level indoors to prevent radon from entering into the STF buildings. <p><i>Regular maintenance for the floor slabs and walls</i></p> <ul style="list-style-type: none"> Cracks and other openings in the foundation should be properly sealed to reduce radon ingress. <p>Sealing the cracks limits the flow of radon into the building thereby making other radon reduction techniques more effective and cost-efficient. It also reduces the loss of conditioned air.</p>	STF buildings / During the design, construction and operation of the STF.	Contractor / STF Operator		N/A N/A N/A			EPD's ProPECC Note PN 1/99 Control of Radon Concentration in New Buildings Appendix 2

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


Table 3. Implementation Schedule of Proposed Waste Management Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.5.1	<p><i>Good Site Practices</i></p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training of site personnel in proper waste management and chemical handling procedures Provision of sufficient waste disposal points and regular collection of waste Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. 	Work site / During the construction period	Contractor		√			Waste Disposal Ordinance (Cap.354) ETWB TCW No. 19/2005
S5.5.1	<p><i>Waste Reduction Measures</i></p> <ul style="list-style-type: none"> Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: 	Work site / During planning & design stage, and construction stage	Contractor		√			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> The design of the foundation works should minimize the amount of excavated material to be generated. Excavated soil should be reused on site as far as possible, e.g. for landscape works, in order to minimize the amount of public fill to be disposed off-site. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans by individual collectors by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force Proper storage and site practices to minimize the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste. 				√			
S5.5.1	<p><i>General Refuse</i></p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.</p>	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk

MaterialLab

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.5.1	<p><i>Construction and Demolition Material</i></p> <p>In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below:</p> <ul style="list-style-type: none"> • A Waste Management Plan, which becomes part of the Environmental Management Plan, should be prepared in accordance with ETWB TCW No.19/2005. • A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed. • In order to monitor the disposal of C&D material at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details. 	Work site / During design stage & construction period	Contractor	√	√			ETWB TCW No. 33/2002 ETWB TCW No. 19/2005 ETWB TCW No. 31/2004
S5.5.1	<p><i>Chemical Waste</i></p> <p>If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible</p>	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste)(General) Regulation)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.							

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des – Design, C – Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


Table 4. Implementation Schedule of Proposed Land Contamination Preventive Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.6.3	<i>Fuel Oil Tank Construction and Test</i> <ul style="list-style-type: none"> The fuel tank to be installed should be of specified durability Double skin tanks are preferable Underground fuel storage tank to be installed should be placed within a concrete pit The concrete pit shall be accessible to allow regular tank integrity tests to be carried out at regular intervals The tank integrity tests should be conducted by an independent qualified surveyor or structural engineer Any potential problems identified in the test should be rectified as soon as possible 	Fuel Oil Storage Tank /	Contractor/ STF Operator	√	√ √ N/A √ √ √			
S5.6.3	<i>Fuel Oil Pipeline Construction and Test</i> <ul style="list-style-type: none"> Installation of aboveground fuel oil pipelines is preferable; if underground pipelines are unavoidable, concrete lined trenches should be constructed to contain the pipelines Double skin pipelines are preferable Distance between the fuel oil refuelling points and the fuel oil storage tank shall be minimized The integrity tests for the pipelines should be conducted by an independent qualified surveyor or structural engineer at regular intervals Any potential problems identified in the test should be rectified as soon as possible 	Fuel Oil Pipelines/ Design, Construction and Operation Phase	Contractor/ STF Operator	√	√ √ √ √			
S5.6.3	<i>Fuel Oil Leakage Detection</i> <ul style="list-style-type: none"> Installation of leak detection device at storage tank and pipelines 	Fuel Oil Storage Tank	Contractor/ STF Operator	N/A	N/A			

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk



Table 5. Implementation Schedule of Proposed Water Pollution Control Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.2	<p>Construction Runoff and Drainage</p> <ul style="list-style-type: none"> Site practices outlined in ProPECC PN 1/94 “Construction Site Drainage” shall be followed as far as practicable in order to minimize surface runoff and the chance of erosion: At the start of site establishment, internal drainage works and erosion and sedimentation control facilities shall be implemented. Channels, earth bunds or sand bag barriers shall be provided on site to direct stormwater to silt removal facilities. The detailed design and installation of the temporary on-site drainage system shall be undertaken by the contractor prior to the commencement of construction. Before commencing any site formation work, all sewer and drainage connections shall be sealed to prevent debris, soil, sand etc. from entering public sewers/drains. Boundaries of earthworks shall be surrounded by dykes or embankments for flood protection, as necessary. Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove sand/silt particles from runoff to meet the standards of the Technical 	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO
					N/A			
					√			
					√			
					√			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>Memorandum under the Water Pollution Control Ordinance. The design of silt removal facilities shall be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures shall be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</p> <ul style="list-style-type: none"> • Water pumped out from foundation piles shall be discharged into silt removal facilities. • During rainstorms, exposed slope/soil surfaces shall be covered by a tarpaulin or other means, as far as practicable. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94. • Exposed soil areas shall be minimized to reduce potential for increased siltation and contamination of runoff. • Earthwork final surfaces shall be well compacted and subsequent permanent work or surface protection shall be immediately performed. Open stockpiles of construction materials or construction wastes on-site of more than 50m³ shall be covered with tarpaulin or similar fabric during rainstorms. • All vehicles shall be cleaned before leaving the works area to ensure no earth, mud and debris is deposited on roads. An adequately designed and 				N/A			
					√			
					√			
					√			
					√			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	sited wheel washing bay shall be provided at every site exit. The wheel washing facility shall be designed to minimize the intake of surface water (rainwater). Wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process.							
S6.7.2	<p><i>General Construction Activities</i></p> <ul style="list-style-type: none"> Debris and refuse generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby water bodies and public drainage system. Stockpiles of cement and other construction materials shall be kept covered when not being used. Oils and fuels shall only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to nearby water bodies and public drains, all fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund shall be drained of rainwater after a rain event. 	Work site / During the construction period	Contractor		√			ProPECC PN 1/94;
S6.7.2	<p><i>Sewage Effluents</i></p> <ul style="list-style-type: none"> Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities. 	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.2	<p><i>Release of PFA Leachate from Ash Lagoon into the Aquatic Environment</i></p> <ul style="list-style-type: none"> Environmental monitoring and audit (EM&A) should be included to ensure that the foundation construction would not cause an unacceptable release of PFA leachate into the Deep Bay waters. The parameters to be measured should include the heavy metals such as cadmium, chromium and aluminium, which have the greatest tendency to leach from the lagooned PFA into the seawater. Details of the measurement requirements are presented in the EM&A manual 	<p>Deep Bay</p> <p>Water outside the Ash Lagoon / During the construction period</p>	Contractor		√			WPCO

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and/or accepted public comment to the proposed project.

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk



Table 6. Implementation Schedule of Proposed Ecological Mitigation Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S7.8.2	Measures to Minimize Disturbance Impact to Wildlife <ul style="list-style-type: none"> • Hoarding of 3m high shall be set up along the boundary of the works areas and associated site access to shield the fauna and breeding population of Little Grebe in the Middle Lagoon from the disturbance impact of machinery. • The works boundaries shall not go beyond the proposed Project Area. All work crews, equipment and human activities shall be confined within the designated works area only. No personnel should encroach or wilfully disturb any wild animals and their habitats. Traffic and human access from the western side of the Project Area should be avoided. • Fencing with climbers or plantation shall be provided, where appropriate, along the STF site boundary and the two sides of access road to screen the surrounding habitats from the STF works areas. 	Boundary of works areas/ Construction Phase Boundary of works areas/ Construction Phase Boundary of works areas/ Operation Phase	Contractor Contractor Contractor		√ √ √			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S7.8.2	<p>Measures to Minimize Impact to natural habitats</p> <ul style="list-style-type: none"> Where practicable, all proposed works shall be conducted in existing built up area to minimize impact to natural habitats. The abutment (permanent structure) for the vehicular bridge shall avoid streambed. The number and size of the temporary supporting structures to be installed over the streambed during construction shall be minimized as far as practicable. The temporarily affected natural habitats, including streambed, shall be reinstated after the completion of works. For affected natural stream section, placement of substrates of similar size and composition to those of original streambed shall be considered to encourage colonization. 	<p>Works areas/ Design and Construction Phase</p> <p>Vehicular bridge/ Design and Construction Phase</p> <p>Works Area/ Operation Phase</p> <p>Works Area/ Operation Phase</p>	<p>STF Designer/ Contractor</p> <p>STF Designer/ Contractor</p> <p>Contractor</p> <p>Contractor</p>	√	√			<p>ETWB TC (Works)</p> <p>No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works</p>
S7.8.2	<p><i>Minimise sedimentation/water quality impacts to waterbodies</i></p> <ul style="list-style-type: none"> Measures to control potential sedimentation/ water quality impacts during the construction phase shall be implemented. To minimize the potential water quality impacts from the construction works located at any river channels, natural streams or seafront, the practices outlined in 	<p>Whole Site/ Construction Phase</p>	<p>Contractor</p>		√			<p>ETWB TC (Works)</p> <p>No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works</p>

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	ETWB TC (Works) No. 5/2005 "Protection of natural streams/rivers from adverse impacts arising from construction works" shall be adopted where applicable.							
S7.8.2	<p><i>Minimize noise disturbance</i></p> <ul style="list-style-type: none"> Noise mitigation measures including the use of quieter piling machinery and construction plants shall be implemented to lower the noise level due to construction works. Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction programme. Machines and plant which may be in intermittent use shall be shut down to a minimum. Plant known to emit noise strongly in one direction, shall be oriented so that the noise is directed away from the Middle Lagoon, where possible. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction period. Mobile plant (such as generator) shall be sited as far away from the Middle Lagoon as possible. Material stockpiles and other structures shall be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Whole Site/ Construction Phase	Contractor		√ √ √ N/A √ √			ETWB TC (Works) No. 5/2005 Protection of natural streams/rivers from adverse impacts arising from construction works

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S7.8.3	<p><i>Measures to Mitigate the Loss of Vegetation</i></p> <ul style="list-style-type: none"> All vegetation located within the work areas shall be preserved as far as practicable. To compensate for the loss of the vegetation and habitats, tree planting shall be provided in the site area where possible. Species chosen for planting shall be similar to the species identified in the survey and be native to Hong Kong or the Southern China. 	Whole Site / Design, Construction and Operation Phase	Contractor / STF Operator	√	√			
S7.8.4	<p>Enhancement Measures to Create Additional Habitat for Little Grebe</p> <ul style="list-style-type: none"> An additional habitat for Little Grebe shall be created in a less disturbed area located at the northeastern part of the proposed STF. The created habitat shall be provided in form of shallow pond(s) incorporating suitable habitat characteristics for Little Grebe. The water level of the created pond shall be kept between 1.5 m to 2 m. Emergent vegetation shall be planted and fish population shall be controlled to allow development of aquatic invertebrate populations as prey of Little Grebe. To screen the created habitat from disturbance due to nearby landfill traffic, planting of native plants shall be provided on the boundary of the pond(s) as appropriate. Prior to construction of the pond(s), detailed Habitat Creation and Management Plan (HCMP) of the created habitat prepared by experienced ecologist(s) with over seven year experience in relevant field shall be circulated to relevant departments including AFCD for comment. 	Within Project Area/ Design Phase, Construction and Operation Phase	Contractor / STF Operator	√	N/A			

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk


Table 7. Implementation Schedule for Landscape and Visual Impact

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 9.4 CM-01	<u>Contaminant/ Sediment Control</u> – Suitable temporary barriers, covers and drainage provisions shall be provided around construction works to avoid discharge of contaminants (such as bleeding from in-situ concrete works) and sediments into sensitive water-based habitats, especially the tidal streams and the mangrove.	Work site / During the construction period	Contractor		√			
Table 9.4 CM-02	<u>Early Planting of Tall Trees</u> – Tall trees proposed under mitigation measure OM-02 shall be planted early, providing visual effect also during construction.	Work site / During the construction period	Contractor		N/A			
Table 9.4 CM-03	<u>Good Site Practice</u> – Construction activities should be restricted to works areas and should be clearly demarcated onsite. Piling of construction materials onsite shall be carefully considered for possible impacts before carrying out.	Work site / During the construction period	Contractor		√			
Table 9.4 CM-04	<u>Existing Trees within Works Areas</u> – All existing trees within work sites shall be properly maintained and protected for their crowns, trunks and roots.	Work site / During the construction period	Contractor	√	√			
Table 9.4 OM-01	<u>Sensitive Bridge Design</u> – The bridge of the proposed access road shall be sensitively designed to minimize impact to the tidal stream and mangrove. It shall be constructed with minimal use of in-situ concreting and with maximum use of precast or prefabricated elements. No pile or support shall be erected within the stream channel.	Bridge of access road / During the design & construction phases	Contractor	√	N/A			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 9.4 OM-02	<u>Tall trees for Chimney</u> – Fast-growing tall trees shall be planted along the east side of the ash-lagoon to counterbalance possible exotic silhouettes, such as from the chimney, of the proposed sludge treatment facilities for sensitive viewers in Pak Nai. The trees shall be planted during the early stage of the construction to ensure effectiveness during operation. They will also help to lessen the visual impact during construction, as already suggested in mitigation measure CM-02.	East side of ash lagoon / During the design & construction phases	Contractor	√	N/A			
Table 9.4 OM-03	<u>Suitable Reinstatement at Ash-lagoon</u> – Affected perimeter of the proposed works area within the ash-lagoon shall be reinstated with suitable planting materials. Traditional reinstatement planting approach for construction projects may not work well for this project. Certain existing grasses and small shrubs have self-seeded the ash- lagoon, demonstrating their tolerance to salts, alkalinity and possible trace metals in the ash. Therefore the same or similar species of vegetation shall be used.	Perimeter of works area / During the design & construction phases	Contractor	√	N/A			
Table 9.4 OM-04	<u>Existing Tree Transplanting</u> – The proposed access roadworks may affect few existing trees, which shall be transplanted as far as practical. A comprehensive tree survey is recommended to locate these trees.	Access road / During the design & operation phases	Contractor	√	N/A			
Table 9.4 OM-05	<u>Planting at Road Intersection</u> – Suitable planting of woodland trees and shrubs shall be provided for the proposed access roadworks at the junction with Nim Wan Road.	Junction of access road with Nim Wan Road / During the design & operation phases	Contractor	√	N/A			

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk


Table 8. Implementation Schedule of Proposed Landfill Gas Hazard Protection Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S10.7.2	Appointment of Safety Officer Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard.	Work Site / During the construction phase	Contractor		√			
S10.7.2	Safety Measures - Excavation Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.	Work Site / During the construction phase	Contractor		√			
S10.7.2	<i>Safety Measures – Welding, Flame-Cutting and Hot works</i> Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, “permit to work” procedures should be followed.	Work Site / During the construction phase	Contractor		√			
S10.7.2	Safety Measures – Enclosed Spaces Site offices or buildings located within WENT Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Enclosed Spaces within WENT Consultant Zone / During the construction phase	Contractor		N/A			
S10.7.2	Safety Measures – Electrical Equipment Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Work Site / During the construction phase	Contractor		N/A			

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division, Tel : +852-2450 8233
 Fugro Development Centre, Fax : +852-2450 6138
 5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
 Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materiallab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S10.7.2	Safety Measures – Piping During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Work Site / During the construction phase	Contractor		N/A			
S10.7.2	Safety Measures – Fire Safety Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be posted around the site warning the anger and potential hazards.	Work Site / During the construction phase	Contractor		√			
S10.7.2	Safety Measures – Confined Spaces Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined Spaces at Work Site / During the construction phase	Contractor		N/A			
S10.7.2	Monitoring Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored shall be set down prior to commencement of ground-works. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 10.6 of the EIA Report.	Work Site / During the construction phase	Contractor		N/A			

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

- Des - Design, C - Construction, O - Operation and Dec – Decommissioning
- N/A – The associated activities are not in progress during the monitoring month, √ - The proposed mitigation measures is implemented

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

The logo for MateriaLab, featuring the word "MateriaLab" in a bold, black, sans-serif font. The text is centered between two thick, horizontal black bars.

Appendix 9

Incident Report on Action Level or Limit Level Non-compliance

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com


MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	25 July 2012
Time	16:08 to 17:36 (Mid-Ebb)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W2: 7.12 (exceed Action Level) W3: 7.04 (exceed Action Level) C1 : 7.22 C2 : 6.86
Possible reason for Action or Limit Level Non-compliance	The exceedance of W2 and W3 was subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 26 July 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com


MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	25 July 2012
Time	16:15 to 16:51 (Mid-Ebb)
Monitoring Location	M1
Parameter	Aluminium
Action & Limit Levels	Action Level : $\geq 20 \mu\text{g/L}$ Limit Level : $\geq 20 \mu\text{g/L}$
Measured Level	M1 – surface : $25 \mu\text{g/L}$ (exceed Limit Level) (at 1m below water surface) M1 – bottom : $22 \mu\text{g/L}$ (exceed Limit Level) (at 1m above the seabed)
Possible reason for Action or Limit Level Non-compliance	Since the pre-bore operation for sheet piling has not commenced yet, so that the exceedance was not caused by the construction work. Heavy rainstorm occurred in the morning, the seabed sediment was stirred up by rainstorm also contributed to the aluminium level at M1. The marine water quality monitoring conducted on 27 July 2012 indicated that the aluminium content returned to $<20 \mu\text{g/L}$. Thus, the exceedance should not be related to the Project.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 07 August 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	27 July 2012
Time	07:35 to 08:47 (Mid-Ebb)
Monitoring Location	W1, W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W1: 7.12 (exceed Action Level) W2: 7.02 (exceed Action Level) W3: 7.07 (exceed Action Level) C1 : 7.49 C2 : 6.97
Possible reason for Action or Limit Level Non-compliance	The exceedance of W1, W2 and W3 was subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)
Signature : 
Date : 31 July 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com


MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	27 July 2012
Time	13:15 to 14:28 (Mid-Flood)
Monitoring Location	W1, W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W1: 7.31 (exceed Action Level) W2: 7.16 (exceed Action Level) W3: 7.10 (exceed Action Level) C1 : 7.23 C2 : 6.81
Possible reason for Action or Limit Level Non-compliance	Heavy rainstorm occurred in 27 July 2012, soil and other runoff were flushed into the river. Rainwater with pH near 7.0 caused the pH at W1, W2 and W3 dropped to below 7.55.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 31 July 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.


Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	30 July 2012
Time	11:13 to 12:27 (Mid-Ebb)
Monitoring Location	W1, W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W1: 7.41 (exceed Action Level) W2: 7.19 (exceed Action Level) W3: 7.36 (exceed Action Level) C1 : 7.27 C2 : 6.95
Possible reason for Action or Limit Level Non-compliance	The exceedance of W1, W2 and W3 was subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)
Signature : 
Date : 31 July 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	01 August 2012
Time	12:36 to 13:51 (Mid-Ebb)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W2: 7.36 (exceed Action Level) W3: 7.31 (exceed Action Level) C1 : 7.44 C2 : 7.02
Possible reason for Action or Limit Level Non-compliance	The exceedance of W2 and W3 was subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 03 August 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED

MaterialLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com


MaterialLab

Our Ref. No. : 100440
Client : VW-VES (HK) Ltd.
Project : Contract No. EP/SP/58/08

Incident Report on Action Level or Limit Level Non-compliance

Project	Sludge Treatment Facilities
Date	22 August 2012
Time	15:41 to 16:48 (Mid-Ebb)
Monitoring Location	W2 and W3
Parameter	pH
Action & Limit Levels	Action Level : ≤ 7.55 or ≥ 8.11 Limit Level : ≤ 6 or ≥ 9
Measured Level	W2: 7.30 (exceed Action Level) W3: 7.42 (exceed Action Level) C1 : 7.21 C2 : 6.92
Possible reason for Action or Limit Level Non-compliance	The exceedance of W2 and W3 was subject to the influent of the low pH from C2.
Actions taken / to be taken	Exceedance was not related to site activities. Ad-hoc monitoring is cancelled.
Remarks	

Prepared by : John Ho (ET Leader)

Signature : 

Date : 23 August 2012

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508233.)

FUGRO TECHNICAL SERVICES LIMITED


MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MateriaLab

Figure 1.1

Construction Works Area

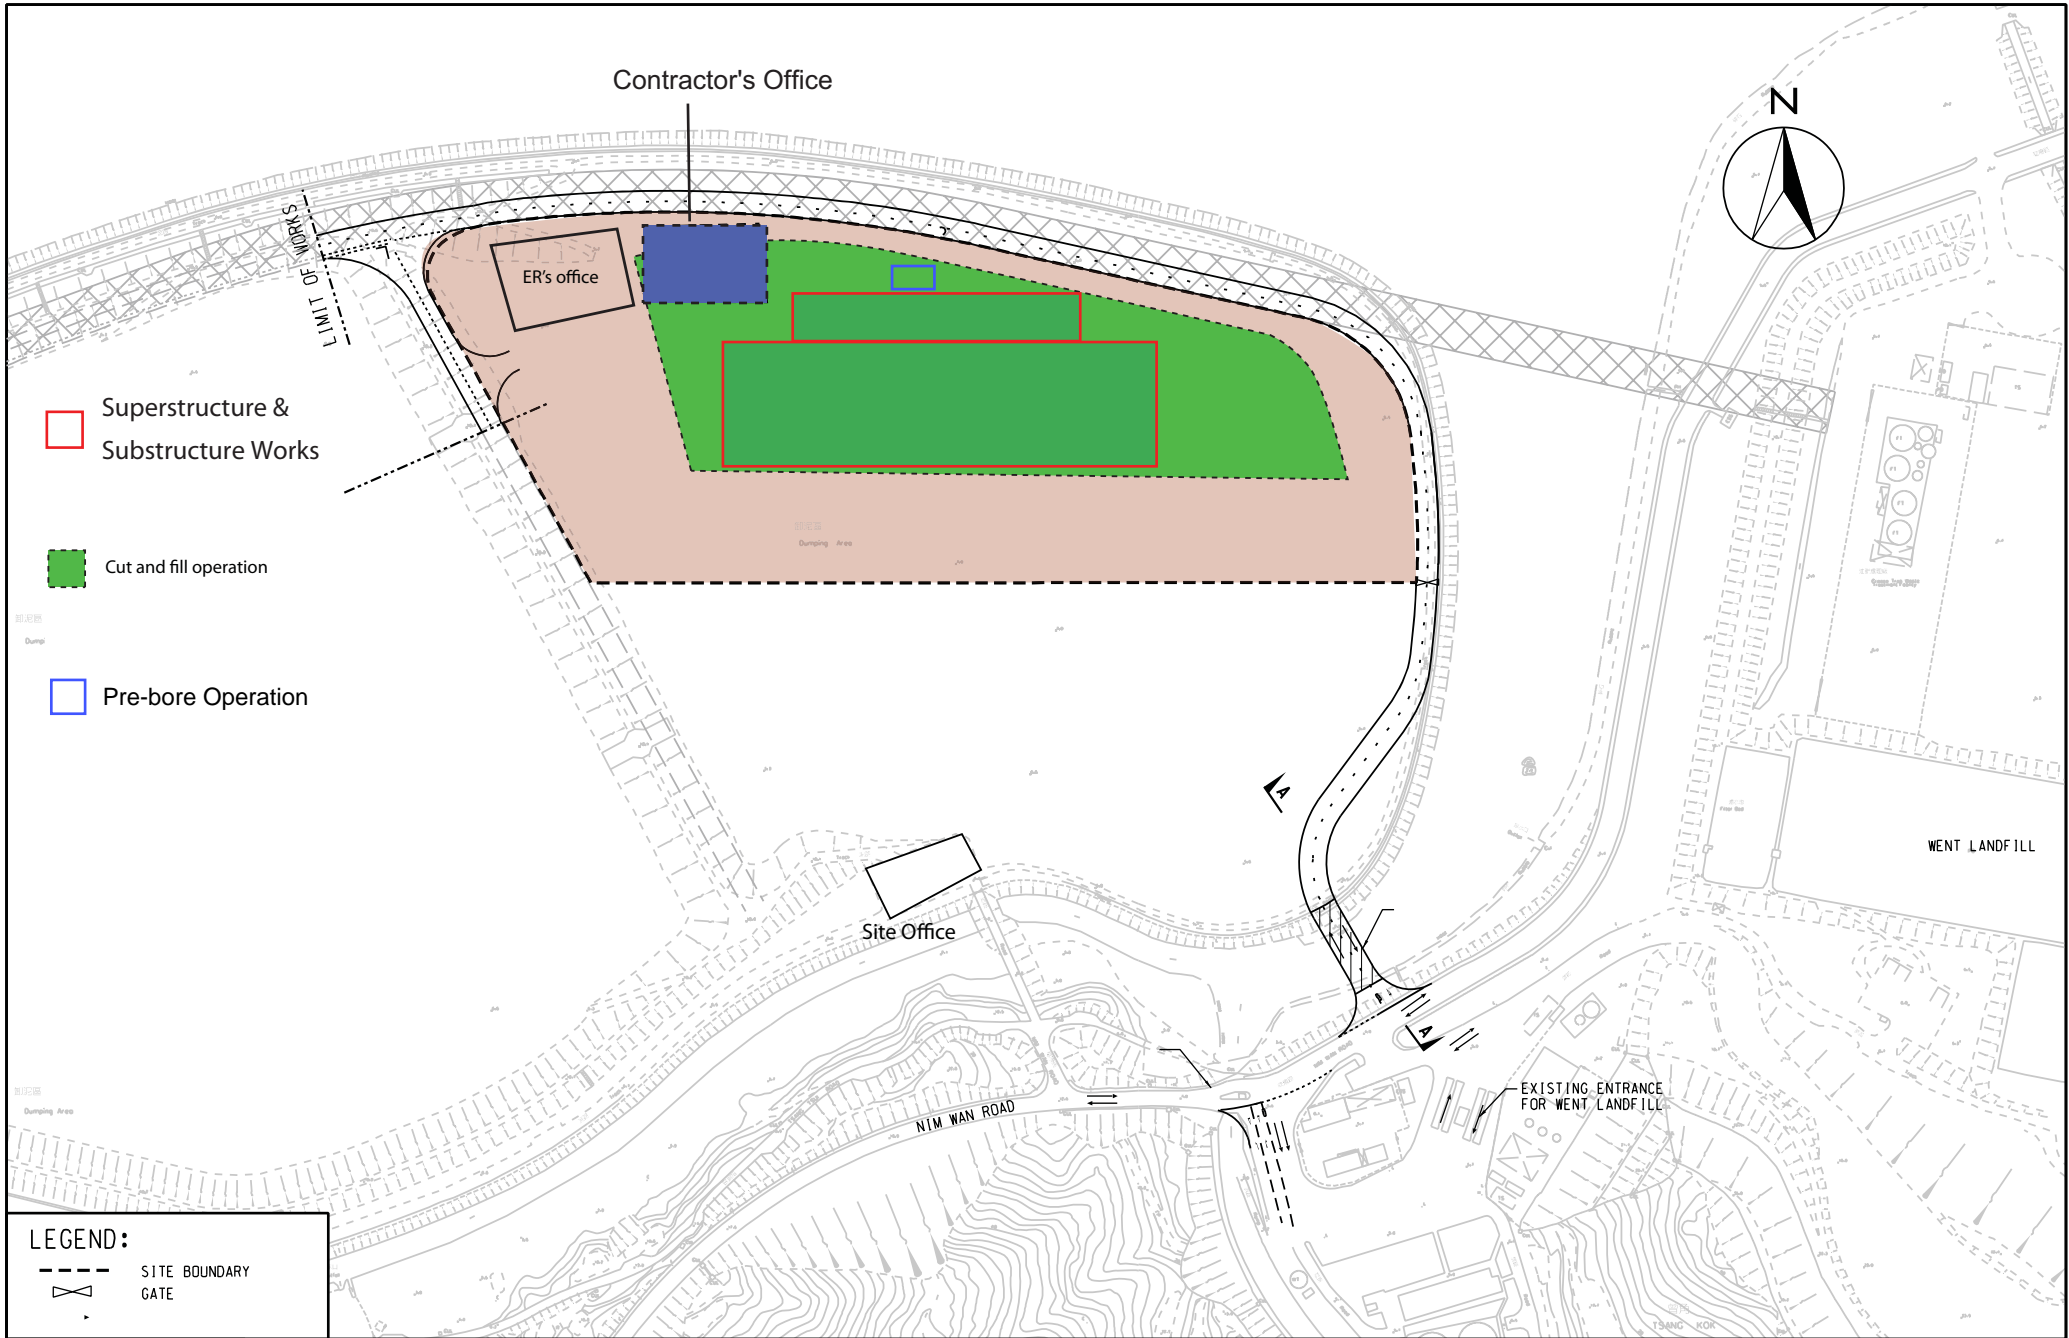


FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MateriaLab

Figure 3.1
Site Layout Plan

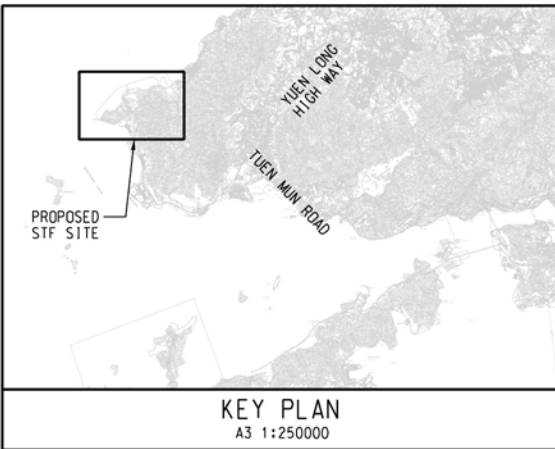

KEY PLAN
A3 1:250000



DEEP BAY

PROPOSED SLUDGE TREATMENT FACILITIES

EXISTING CLP ASH LAGOON AT TSANG TSUI

WENT LANDFILL

大水坑 831250 N
Tai Shui Hong

BLACK POINT POWER STATION

TSANG KOK STREAM

BLACK POINT

830000 N

URMSTON ROAD

配水庫
Ser Res

龍鼓上棚
Lung Au
Sheung Tan

807500 E

808750 E

810000 E

811250 E

DATE: GUOXH 2008-9-30

MAUNSELL | AECOM
Metcalf & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY
LOCATION PLAN OF PROPOSED SLUDGE TREATMENT FACILITIES

SCALE	A3 1:12500	DATE	SEP. 2008
CHECK	PPMY	DRAWN	XCF
JOB No.	60015756	DRAWING No.	FIGURE 1.1
		REV	-

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



MateriaLab

Figure 3.2

WENT Landfill Gas Control Zone



SECTION OF NULLAH
WHERE WATER IS ALWAYS
PRESENT

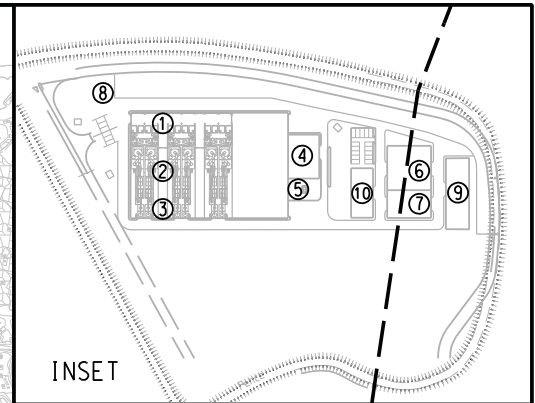


LEGEND

- ① DELIVERY BAY
- ② INCINERATORS AND AIR CONTROL EQUIPMENT
- ③ FUEL GAS RESIDUE SILOS, ASH SILOS & LOADING AREA
- ④ CHEMICAL / FUEL STORAGE AND FEEDING
- ⑤ STACK
- ⑥ ADMINISTRATION BUILDING & LABORATORY
- ⑦ MAINTENANCE WORKSHOP
- ⑧ UTILITY YARD
- ⑨ DESALINATION PLANT, SEAWATER PUMPING STATION & STORAGE TANK
- ⑩ SEWAGE TREATMENT WORKS

WENT LANDFILL
CONSULTATION ZONE
BOUNDARY

WENT LANDFILL
WASTE BOUNDARY

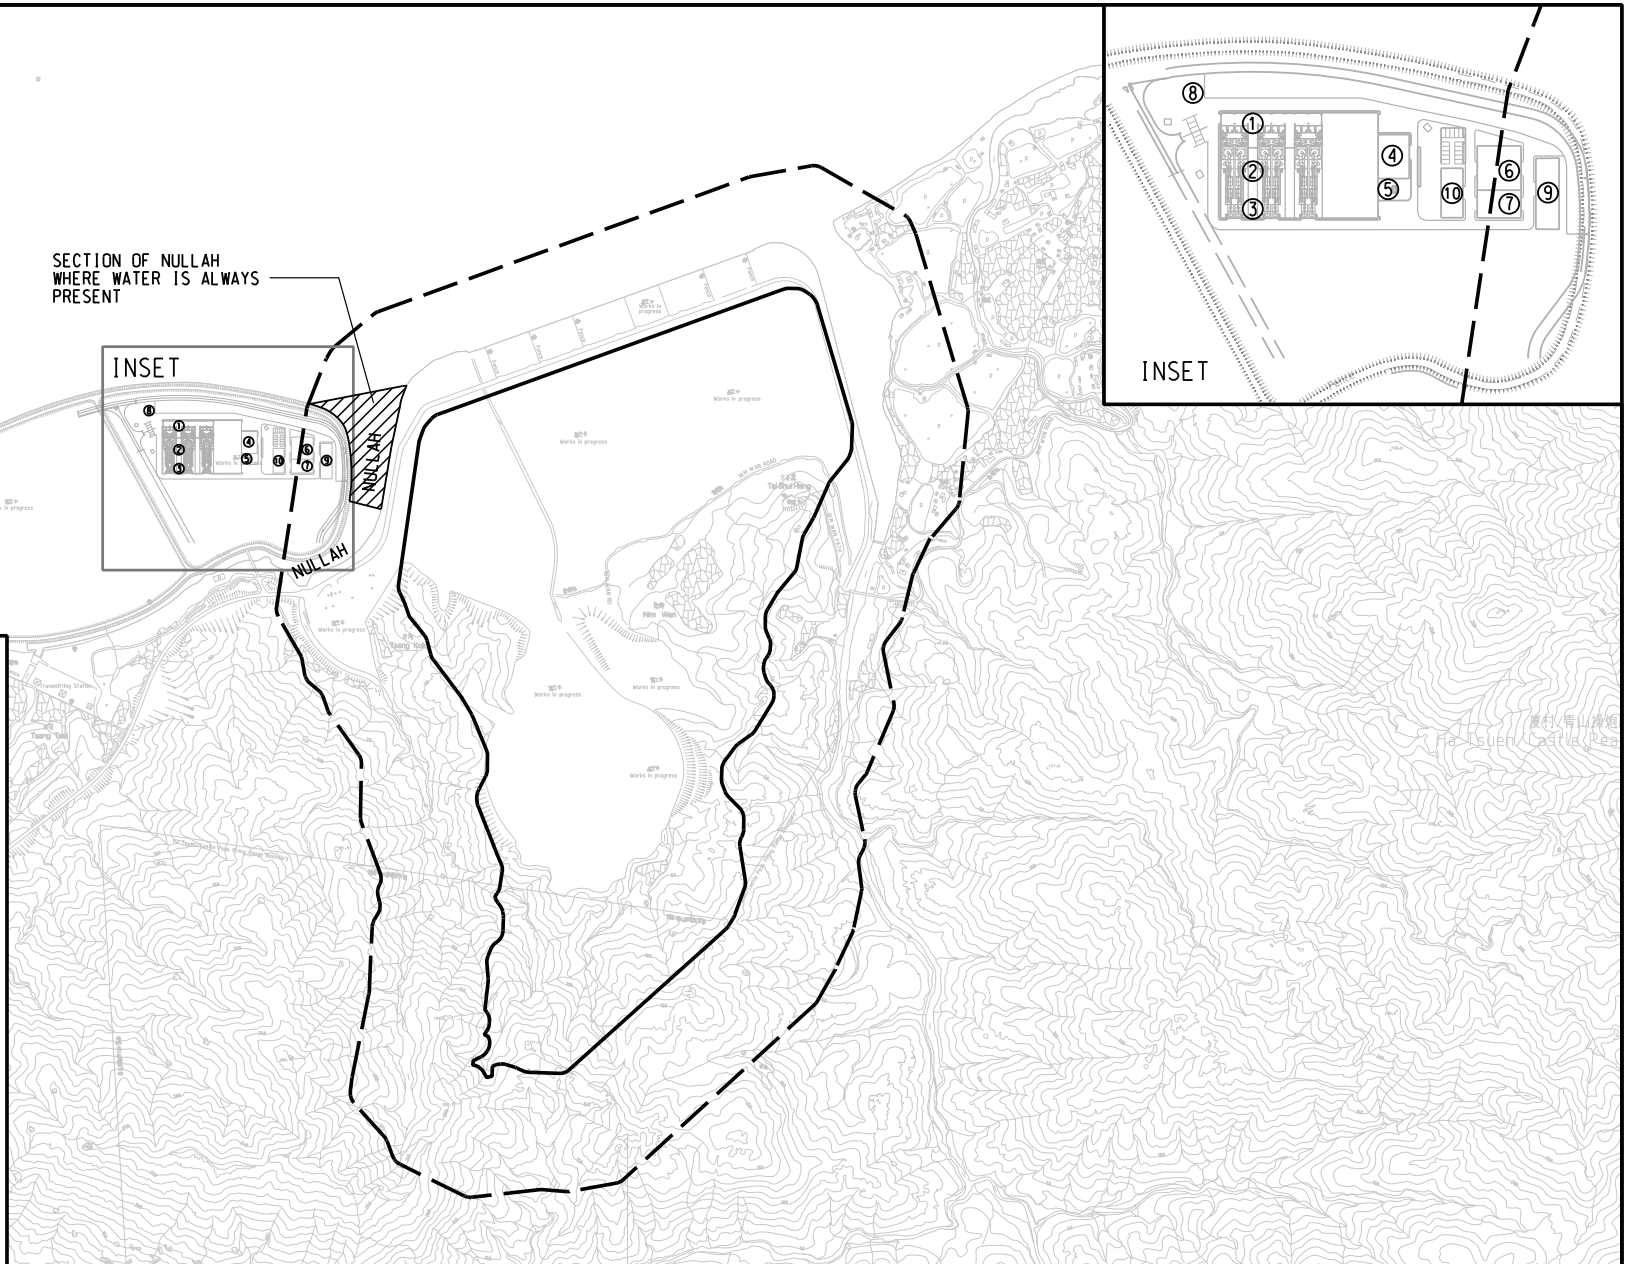

DATE: \$DATE\$

MAUNSELL | AECOM
Metcalf & Eddy Ltd.

AGREEMENT NO. CE 28/2003 (EP)
SLUDGE TREATMENT FACILITIES - FEASIBILITY STUDY
WENT LANDFILL CONSULTATION ZONE

SCALE	1:11000	DATE	APR. 2008
CHECK	TCYC	DRAWN	ALFA
JOB No.	60039510	DRAWING No.	FIGURE 10.1
		REV	-

INSET

BUNKERFFERDAM

831540.261 N
810555.162 E

Portion 1 (next to Plant B)

Portion 3 (next to Canteen) -
(i) Backfill on 11 July 2012
(ii) Resume excavation on 26 July 2012


831408.992 N
810534.890 E

Portion 1 (next to Water
Treatment) - Backfill on 07
July 2012

Portion 3 (next to
T758)

831251.868 N
810511.028 E

WENTNDFILL
CONSULTATIONNE
BOUNDARY

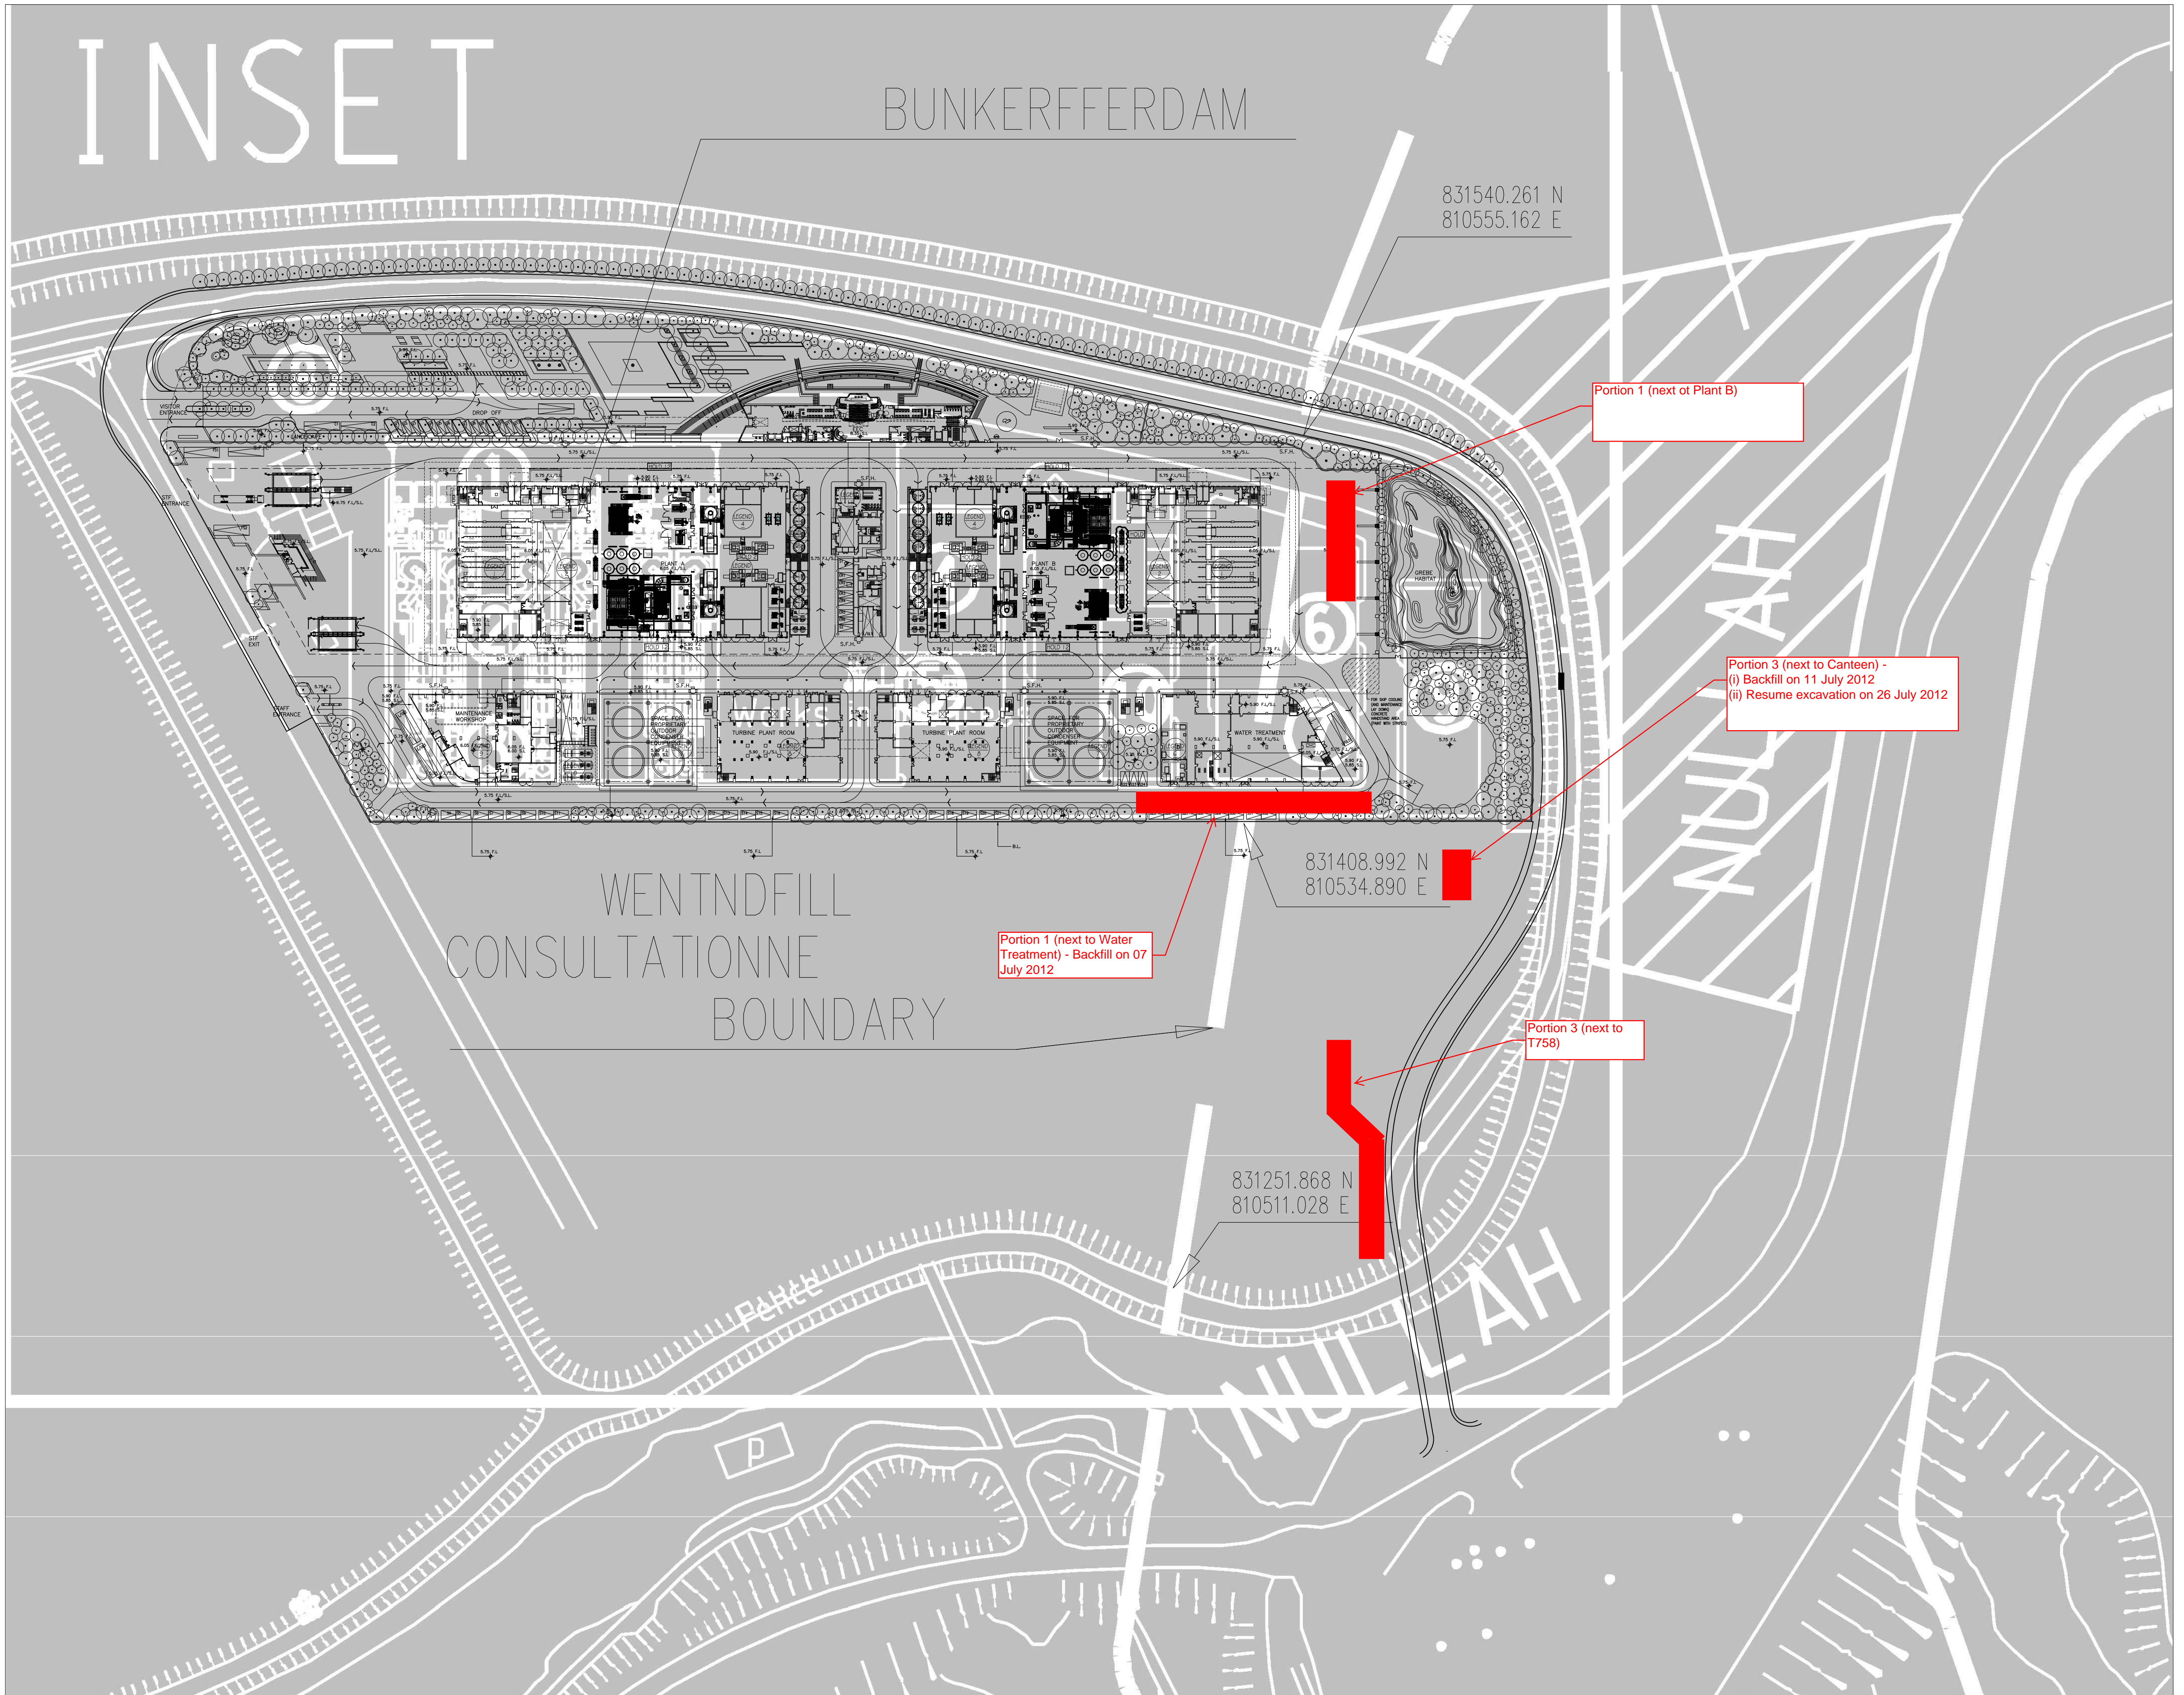

INSET

BUNKERFFERDAM

831540.261 N
810555.162 E

Portion 1 (next to Plant B)

Portion 1 (next to Plant B)
- concreting on 08 August 2012

Portion 3 (next to Canteen) - backfilled on 15 August 2012.

Portion 3 (next to Canteen)


831408.992 N
810534.890 E

Backfilled on 01 August 2012

Portion 3 (next to T758)

831251.868 N
810511.028 E

WENTNDFILL
CONSULTATIONNE
BOUNDARY

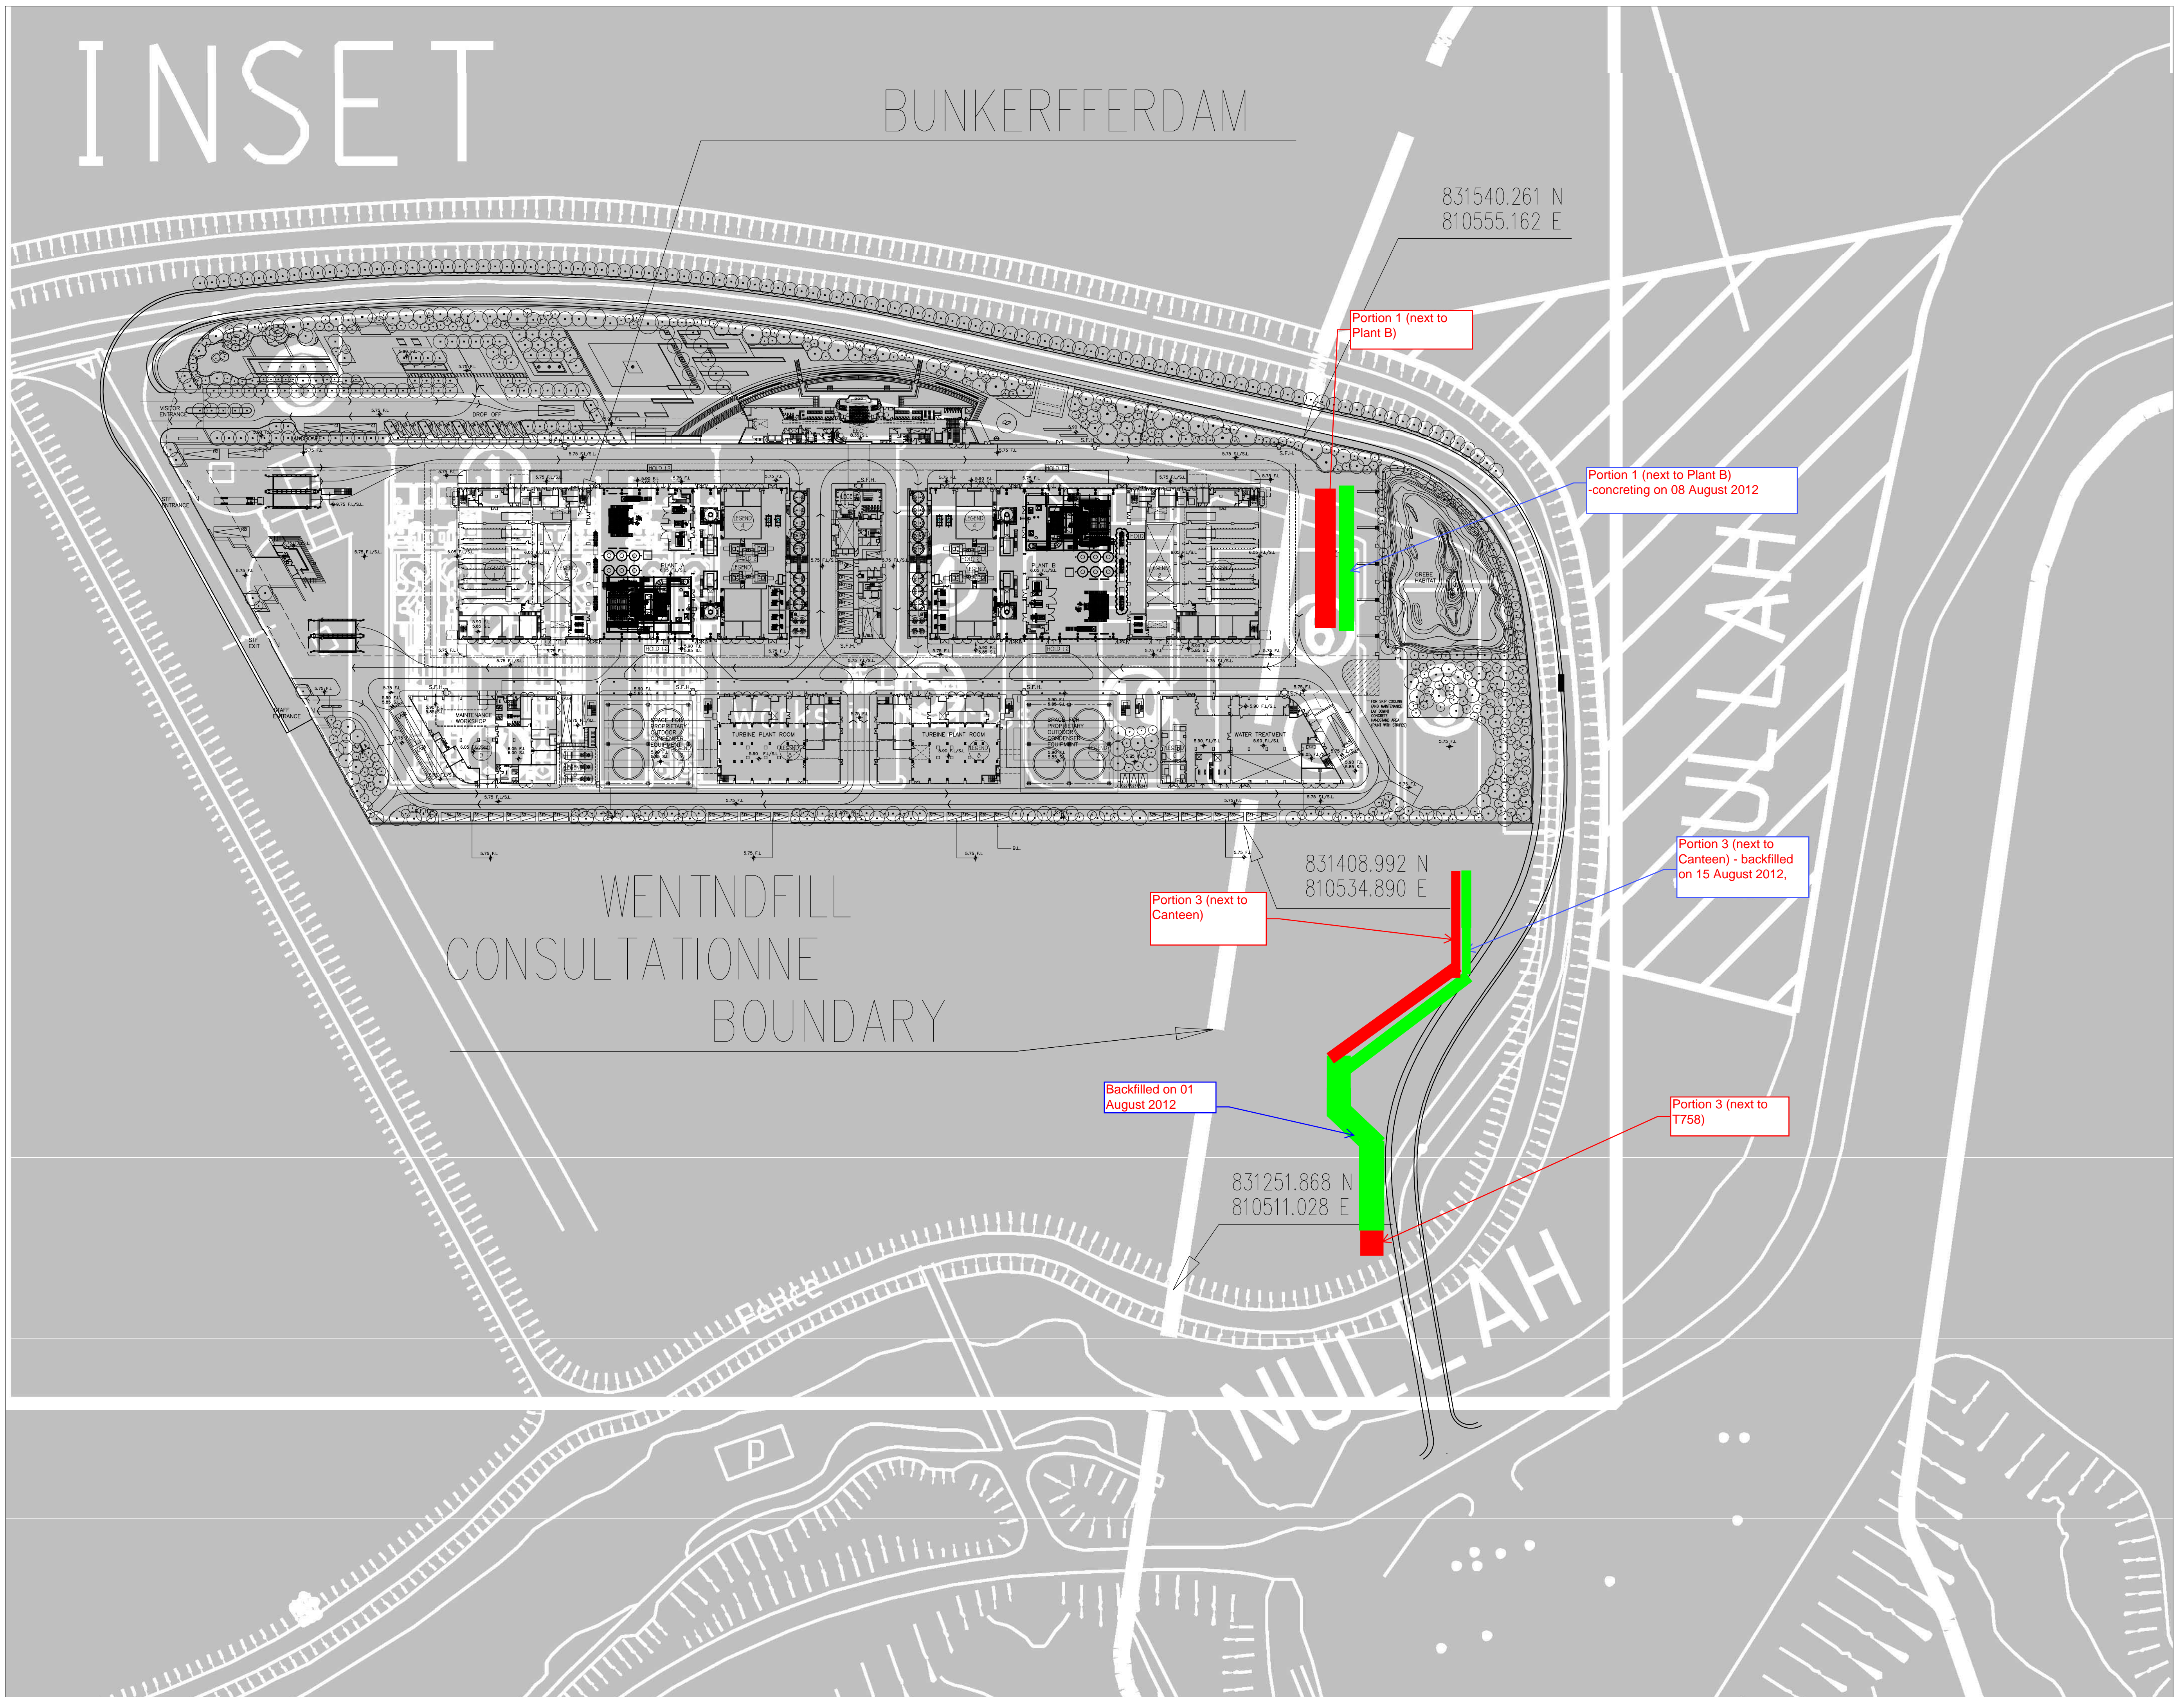

FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

MateriaLab

Figure 4.1

Ecological Transect Route

0m 100m 200m 300m 400m




DEEP BAY

EXISTING CLP ASH LAGOON
AT TSANG TSUI


PROPOSED SLUDGE
TREATMENT FACILITIES

- Notes:
- Survey Route
 - Middle Lagoon Boundary
 - - - 20m from Middle Lagoon Boundary

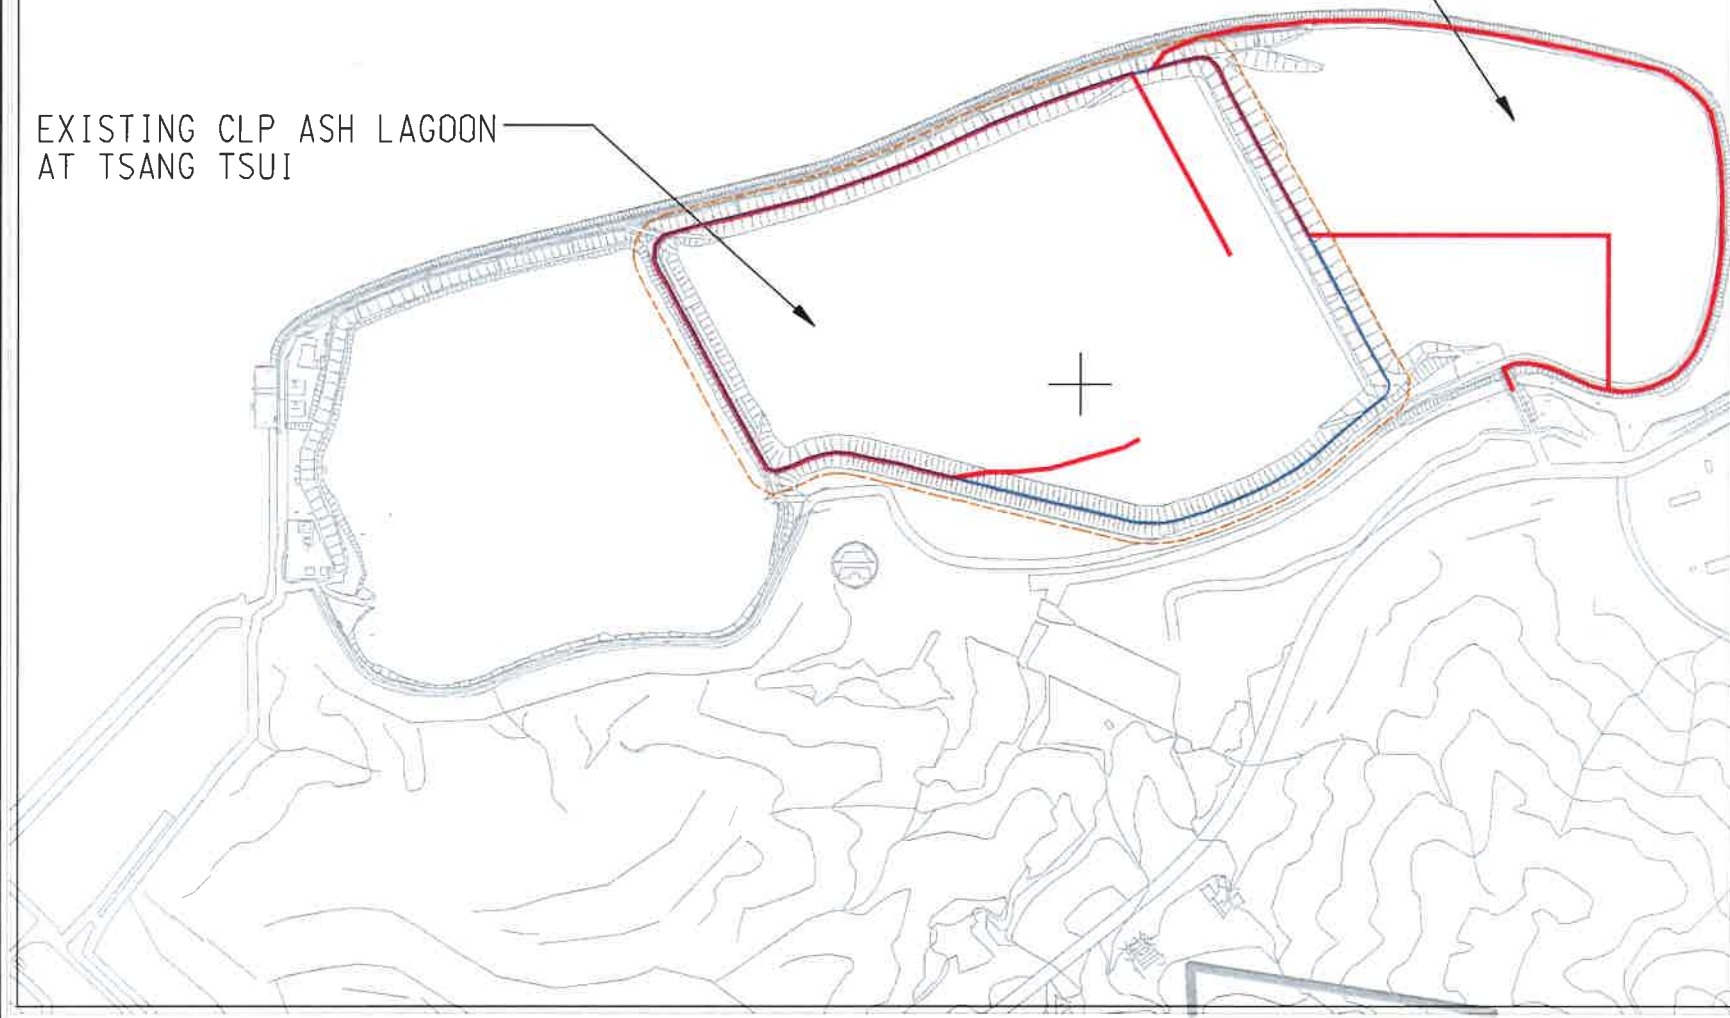

Asia Ecological Consultants Ltd

Project Title:
**Contract No. EP/SP/58/08
Sludge Treatment Facilities**



Drawing Title:
Ecological Transect Route

Drawn: SK	Scale: As shown
Checked: DJS	Date: May 2011
Approved: DJS	File: --
Drawing Number: --	Revision 1
