

東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong  
Tel : 2695 8318 E-mail : etl@ets-testconsult.com  
Fax : 2695 3944 Web site : www.ets-testconsult.com

## **HKPFH Joint Venture**

**Contract No.: CV/2013/06  
Handling of Surplus Public Fill  
(2014-2016)**

**TUEN MUN AREA 38 FILL BANK**

**MONTHLY EM&A REPORT NO.5**

**(MAY 2014)**

Prepared by:

LAW, Sau Yee  
Senior Environmental Officer

Checked by:

LAU, Chi Leung  
Environmental Team Leader

Issue Date: 13 June 2014

Report No.: ENA40936

Ref.: CEDPFRSFEM01\_0\_0102L.14

16 June 2014

By E-mail and Fax No.: 2695 3944

ETS-Testconsult Limited  
8/F, Block B  
Veristrong Industrial Centre  
34-36 Au Pui Wan Street  
Fo Tan, Hong Kong

Attention: Mr. C L Lau

Dear Mr. Lau,


**Re: Contract No. CV/2013/06  
Handling of Surplus Public Fill (2014 – 2016)  
Monthly EM&A Report (No. 5) for May 2014  
for the Tuen Mun Area 38 Fill Bank**

Reference is made to your submission of the revised draft Monthly EM&A Report for May 2014 for the TM Area 38 Fill Bank received by E-mail on 16 June 2014.

We are pleased to inform you that we have no comment on the captioned report.

Thank you very much for your attention and please do not hesitate to contact our Jason Lai or the undersigned should you have any queries.

Yours sincerely,



Tony Cheng  
Independent Environmental Checker

c.c. CEDD Attn: Mr. Jason Wong / Mr. Terry Chock / Mr. N C Chan Fax No.: 2714 0113  
HKPFHJV Attn: Mr. Jerry Siu / Mr. Eric Wan Fax No.: 2744 6937

Q:\Projects\CEDPFRSFEM01\02 Project Management\02 Corr\CEDPFRSFEM01\_0\_0102L.14.doc



<b>TABLE OF CONTENTS</b>		<b>Page</b>
<b>EXECUTIVE SUMMARY</b>		
<b>1.0</b>	<b>INTRODUCTION</b>	<b>1</b>
<b>2.0</b>	<b>PROJECT INFORMATION</b>	
	2.1 Construction Programme	1
	2.2 Project Organization and Management Structure	1
	2.3 Contact Details of Key Personnel	1
<b>3.0</b>	<b>CONSTRUCTION PROGRESS IN THIS REPORTING MONTH</b>	<b>2</b>
<b>4.0</b>	<b>AIR QUALITY MONITORING</b>	
	4.1 Monitoring Requirement	2
	4.2 Monitoring Equipment	2
	4.3 Monitoring Parameters, Frequency and Duration	2
	4.4 Monitoring Locations and Schedule	2
	4.5 Monitoring Methodology	3
	4.6 Action and Limit levels	3 – 4
	4.7 Event-Action Plans	4
	4.8 Results and Observations	4
<b>5.0</b>	<b>MARINE WATER QUALITY MONITORING</b>	
	5.1 Monitoring Requirements	4
	5.2 Monitoring Locations	4
	5.3 Monitoring Parameters and Frequency	4
	5.4 Monitoring Methodology and Equipment Used	5 – 6
	5.5 Action and Limit Levels	6
	5.6 Event and Action Plan	7
	5.7 Monitoring Duration and Period in this reporting month	7
	5.8 Marine Water Monitoring Results	7
<b>6.0</b>	<b>NOISE MONITORING</b>	
	6.1 Monitoring Requirements	7
	6.2 Monitoring Equipment	8
	6.3 Monitoring Parameters, Duration and Frequency	8
	6.4 Monitoring Locations and Period	8
	6.5 Monitoring Procedures and Calibration Details	8 – 9
	6.6 Action and Limit levels	9
	6.7 Event-Action Plans	9
	6.8 Results and Observation	9
<b>7.0</b>	<b>ENVIRONMENTAL AUDIT</b>	
	7.1 Weekly Site Inspection	9
	7.2 Review of Environmental Monitoring Procedures	10
	7.3 Status of Environmental Licensing and Permitting	10
	7.4 Implementation Status	10 – 11
<b>8.0</b>	<b>LANDSCAPE AND VISUAL</b>	<b>11</b>
<b>9.0</b>	<b>WASTE MANAGEMENT</b>	
	9.1 Summary of Waste disposed of in this month	11
	9.2 Advice on the Solid and Liquid Waste Management Status	11 – 12
<b>10.0</b>	<b>ENVIRONMENTAL NON-CONFORMANCE</b>	
	10.1 Summary of air quality, noise and marine water quality	12
	10.2 Summary of Environmental Complaints	12
	10.3 Summary of Notification of Summons and Prosecution	12
<b>11.0</b>	<b>CONCLUSIONS AND RECOMMENDATIONS</b>	<b>12 – 13</b>
<b>12.0</b>	<b>FUTURE KEY ISSUE</b>	<b>13</b>



## APPENDIX

A	Organization Chart and Lines of Communication
B1	Calibration Certificates for Impact Air Quality Monitoring Equipments
B2	Impact Air Quality Monitoring Results
B3	Graphical Plots of Impact Air Quality Monitoring Data
C1	Calibration Certificates for Impact Marine Water Quality Monitoring Equipments
C2	Impact Marine Water Quality Monitoring Results
C3	Graphical Plots of Impact Marine Water Quality Monitoring Data
D1	Calibration Certificates for Impact Noise Monitoring Equipments
D2	Impact Noise Monitoring Results
D3	Graphical Plots of Impact Noise Monitoring Data
E	Weather Condition
F	Event-Action Plans
G	Construction Programme
H	Weekly ET's Site Inspection Record
I	Implementation Schedule of Mitigation Measures
J	Site General Layout Plan
K	QA/QC Results of Laboratory Analysis
L	Complaint Log

## FIGURES

Figure 1	Locations of Air Quality Monitoring Stations – Tuen Mun Area 38 Fill Bank
Figure 2	Locations of Water Quality Monitoring Stations – Tuen Mun Area 38 Fill Bank
Figure 3	Locations of Noise Quality Monitoring Stations – Tuen Mun Area 38 Fill Bank

## TABLES

2.1	Contact Details of Key Personnel
4.1	Air Quality Monitoring Equipment
4.2	Monitoring parameters, duration and frequency of air quality monitoring
4.3	Action and Limit levels for 24-hr TSP and 1-hr TSP
5.1	Monitoring Parameters and Frequency of the marine water
5.2	Summary of testing procedure
5.3	Details of Water Quality Monitoring Equipment (In-site measurement)
5.4	Water Quality Action and Limit Levels
5.5	Time Schedule of Water Quality Monitoring
5.6	Summary of Marine Water Quality Exceedances in this reporting month
6.1	Noise Monitoring Equipment
6.2	Duration, Frequencies and Parameters of Noise Monitoring
6.3	Action and Limit Levels for noise monitoring
7.1	Key Findings of Weekly ET Site Inspections in this reporting month
7.2	Summary of environmental licensing and permit status
7.3	Summary of Environmental Complaints and Prosecutions
9.1	Actual amounts of waste generated in this reporting month



## **EXECUTIVE SUMMARY**

This monthly Environmental Monitoring and Audit (EM&A) report No.5 was prepared by Environmental Team (ET) of ETS-Testconsult Ltd (ETL) for the "Contract No. CV/2013/06 Handling of Surplus Public Fill (2014-2016) – Tuen Mun (TM) Area 38 Fill Bank" (The Project).

This report documented the findings of EM&A Works conducted during the operation phase of Fill Bank at TM Area 38 in May 2014.

### **Site Activities**

As informed by the Contractor, the site activities in this reporting period were as below:

- *Operation of the TM38 Fill Bank.*
- *Transferring public fill to vessel and delivering to Taishan and other parties.*
- *Construction of new wheel washing bay.*
- *Installation of Project Sign Board.*

### **Environmental Monitoring Progress**

The summary of the monitoring activities in this monitoring month is listed below:

- *24-hour TSP Monitoring: 5 Occasions at 2 designated locations*
- *1-hour TSP Monitoring: 16 Occasions at 2 designated locations*
- *Noise, Daytime: 9 Occasions at 2 designated locations*
- *Marine Water Quality Monitoring: 12 Occasions at 4 designated locations*
- *Weekly-site inspection: 4 Occasions*

### **Air Monitoring**

No exceedance of Action and Limit level was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

### **Noise Monitoring**

No exceedance of Action and Limit level for noise monitoring was recorded in the reporting month.

### **Marine Water Quality Monitoring**

According to the marine water monitoring results, no exceedance of Action and Limit level was recorded.

### **Weekly Site Inspection**

In general, performance on environmental mitigation measures implemented was found to be satisfactory in this reporting month. The major findings observed during site inspections are presented in the Section 7.0.

### **Environmental Complaints, Notification of summons and successful prosecutions**

No complaint, notification of summon and prosecution with respect to environmental issues was received in this monitoring month.

### **Future Key Issues**

Based on the site inspections and forecast of engineering works in the coming month, key issues to be considered are as follows:

- *Dust generation from activities on site, such as vehicular movements along unpaved area and rock crushing activities;*
- *Noise impact from operating equipment and machinery on site;*
- *Wastewater and surface runoff from the site discharged into nearby water body; and*
- *Storage and usage of chemicals / fuel and chemical waste / waste oil.*



## 1.0 INTRODUCTION

HKPFH Joint Venture (HKPFH-JV) appointed Environmental Team (ET) of ETS-Testconsult Limited (ETL) to undertake the Environmental Monitoring and Audit (EM&A) for the “Contract No: CV/2013/06 – Handling of Surplus Public Fill (2014-2016) – Tuen Mun (TM) Area 38 Fill Bank” (The Project).

In accordance with the Condition 5 of Part C of Environmental Permit (No.: EP-210/2005/B) (the EP), an EM&A programme as set out in the Project Profile should be implemented.

The EM&A programme requires environmental monitoring for air quality, water quality and environmental site inspections for air quality, water quality, landscape and visual, and waste management. The EM&A requirements for each parameter described in the following sections include:

- All monitoring parameters;
- Monitoring schedules for the reporting month and forthcoming months;
- Action and Limit levels for all environmental parameters;
- Event/Action Plans;
- Environmental mitigation measures, as recommended in the Project Profile; and
- Environmental requirements in contract documents.

Baseline monitoring was completed in May 2003 by Stanger Asia Ltd. Action and Limit Levels were established for air and water quality parameters based on the baseline monitoring results.

This report documented the findings of EM&A Works conducted during the operation phase of Fill Bank at Tuen Mun Area 38 in May 2014.

## 2.0 PROJECT INFORMATION

### 2.1 Construction Programme

Details of construction programme are shown in Appendix G.

### 2.2 Project Organization and Management Structure

The organization chart and lines of communication with respect to the on-site environmental management and monitoring program are shown in Appendix A.

### 2.3 Contact Details of Key Personnel

The key personnel contact names and telephone numbers are shown in Table 2.1.

Table 2.1 Contact Details of Key Personnel

Organization	Name of Key Staff	Project Role	Tel. No.	Fax No.
CEDD	Mr. P C Mok Mr. K C Wong Mr. C T Chock Mr. Y F Kwong	Engineer's Representative	2762 5514	2714 0113
IEC (ENVIRON)	Mr Tony Cheng	IEC	3465 2888	3465 2899
Contractor (HKPFH-JV)	Mr. K W Li	Project Manager	9750 6438	2744 6937
ET (ETL)	Mr C. L. Lau	ET Leader	2946 7791	2695 3944



### 3.0 CONSTRUCTION PROGRESS IN THIS REPORTING MONTH

As informed by the Contractor, the activities in the reporting month include:

- Operation of the TM38 Fill Bank.
- Transferring public fill to vessel and delivering to Taishan and other parties.
- Construction of new wheel washing bay.
- Installation of Project Sign Board.

### 4.0 AIR QUALITY MONITORING

#### 4.1 Monitoring Requirement

1-hr and 24-hr TSP levels were monitored in the reporting month. Table 4.3 shows the Action and Limit Levels for the environmental monitoring works.

#### 4.2 Monitoring Equipment

Both 1-hour and 24-hour TSP air quality monitoring was performed using a GMWS2310 High Volume Air Sampler (HVS) located at each of the designated monitoring station. Table 4.1 summarizes the equipment used in the air quality monitoring programme. Copies of the calibration certificates for the HVS and calibrator are attached in Appendix B1.

Table 4.1 Air Quality Monitoring Equipment

<i>Equipment</i>	<i>Model and Make</i>
<i>HVS</i>	<i>Greasby GMWS2310</i>
<i>Calibrator</i>	<i>Tisch TE-5025A</i>

#### 4.3 Monitoring Parameters, Frequency and Duration

Table 4.2 summarizes the monitoring parameters, monitoring duration and frequencies of air quality monitoring.

Table 4.2 Monitoring parameters, duration, frequency of air quality monitoring

<i>Parameter</i>	<i>Duration</i>	<i>Frequency</i>
<i>24-hr TSP</i>	<i>24 hr</i>	<i>Once per six days</i>
<i>1-hr TSP</i>	<i>1 hr</i>	<i>Three times per six days</i>

#### 4.4 Monitoring Locations and Schedule

In accordance with the Project Profile, two air-quality monitoring stations, namely TM-A1 and TM-A2, were selected for the 1-hr TSP and 24-hr TSP sampling.

Since the area for existing air monitoring station TM-A2 near Tipping Hall No.1 was handed over to EcoPark, air monitoring station TM-A2 was cancelled and the air monitoring was carried out at an alternative air monitoring station TM-RA2 (refer to Figure 1 attached) from 28 October 2008.

The locations of monitoring stations are shown in Figure 1.

During the reporting month, 1-hr and 24-hr TSP monitoring were carried out as the schedule. The details for 24-hr and 1-hr TSP monitoring carried out in this reporting month are summarized in Appendix B2.



## 4.5 Monitoring Methodology

### *Both 1-hr and 24-hr air quality monitoring (High Volume Sampler)*

#### Instrumentation

High volume sampler, as HVS, (Greasby GMWS2310) complete with appropriate sampling inlets were employed for both 1-hour and 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

#### Installation

The installation of HVS refers to the requirement stated in Appendix D2 "General Technical Requirements of Environmental Monitoring" in the Environmental Monitoring and Audit Guidelines for Development Projects in Hong Kong published by EPD.

#### Operation/Analytical Procedures

Operating/analytical procedures for the operation of HVS are as below:

- Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6m<sup>3</sup>/min and 1.7m<sup>3</sup>/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. The flow rate is indicated on the flow rate chart.
- For TSP sampling, fiberglass filters (GA-55) were used.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated 5 minutes to establish thermal equilibrium before placing any filter media at designated air monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an air-tight seal on the outer edges of the filter. Then the filter holder frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The programmable timer will be set for a sampling period of 1 hour / 24 hours. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number.).
- After sampling, the filter was transferred from the filter holder of the HVS to a sealed plastic bag and sent to the laboratory for weighting. The elapsed time was also recorded.
- Before weighting, all filters were equilibrated in a desiccator for 24 hour with the temperature of 25°C ± 3°C and the relative humidity (RH) <50% ±5%.

#### Maintenance & Calibration

- The HVS and their accessories should be maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVS should be calibrated at bi-monthly intervals.

#### *Wind Data Monitoring*

Wind data included wind speed and wind direction were directly extracted from Tuen Mun Station of Hong Kong Observatory during this reporting month. The wind data are presented in Appendix E.

## 4.6 Action and Limit Levels

Table 4.3 shows the Action and Limit levels for 24-hr TSP and 1-hr TSP monitoring.





Table 4.3 Action and Limit Levels for 24-hr TSP and 1-hr TSP

Monitoring Location	24-hr TSP ( $\mu\text{g}/\text{m}^3$ )		1-hr TSP ( $\mu\text{g}/\text{m}^3$ )	
	Action Level	Limit Level	Action Level	Limit Level
TM-A1	192	260	344	500
TM-RA2 *	192	260	344	500

Remark (\*): Since the area for existing air monitoring station TM-A2 near Tipping Hall No.1 was handed over to EcoPark, air monitoring station TM-A2 was cancelled and the air monitoring was carried out at an alternative air monitoring station TM-RA2 from 28 October 2008. Since dust monitoring stations TM-A2 and TM-RA2 are located close to the major dust emission sources and no significant difference between them on the prevailing meteorological conditions, the baseline data from TM-A2 can also be valid in the case of TM-RA2.

#### 4.7 Event-Action Plans

Please refer to Appendix F for details.

#### 4.8 Results and Observations

All monitoring data of both 1-hr and 24-hr TSP monitoring is provided in Appendix B2. Graphical presentation of 1-hr and 24-hr TSP monitoring results for the reporting month is shown in Appendix B3. Wind data, including wind speed and wind direction, are annexed in Appendix E.

No exceedance of Action and Limit level was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

Generally, the Contractor implemented sufficient dust mitigation measures, including operation of wheel washing facilities and road dampening by water bowsers on the main haul roads and unpaved areas.

### 5.0 MARINE WATER QUALITY MONITORING

#### 5.1 Monitoring Requirements

In accordance with the Project Profile, impact marine water quality monitoring was conducted three days per week. Measurements were taken at both mid-flood and mid-ebb tides at three depths (i.e. 1m below surface, mid depth and 1m from seabed) at two control monitoring stations (TM-FC1 and TM-FC2) and two impact monitoring stations (TM-FM1 and TM-FM2).

#### 5.2 Monitoring Locations

As stipulated in the EM&A requirement, there were four monitoring stations undertaken during the impact monitoring. Figure 2 shows the locations of the marine water quality monitoring stations.

#### 5.3 Monitoring Parameters and Frequency

Monitoring of the marine water quality parameters and frequency are listed in Table 5.1.

Table 5.1 Monitoring Parameters and Frequency of the marine water

Monitoring Station	Parameter	Frequency	No. of Depths
Control Stations: TM-FC1 (Mid-ebb) and TM-FC2 (Mid-flood)	Depth (m)	3 days/week, 2 tides/day	3 (Surface, mid- depth & bottom)
	Temperature ( $^{\circ}\text{C}$ )		
	Dissolved Oxygen (mg/L and % saturation)		
	Turbidity (NTU)		
	Salinity (ppt)		
Impact Stations: TM-FM1 and TM-FM2	Suspended solids (mg/L)		



## 5.4 Monitoring Methodology and Equipment Used

### For Location of the monitoring stations

#### **Global Positioning System (GPS)**

A hand-held digital GPS was used to identify the designated monitoring stations prior to water sampling.

### For Water Depth measurement

#### **Echo Sounder**

A portable, battery-operated echo sounder was used for the determination of water depth at each designated monitoring station.

### For In-situ Water Quality Measurement

All in-situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals or sometimes longer throughout all stages of the water quality monitoring.

#### **Dissolved Oxygen, Salinity and Temperature Measuring Equipment**

A portable, weatherproof dissolved oxygen & salinity measuring instrument, which complete with cable, sensor and DC power source (e.g. YSI 85 or equivalent) was used for measuring:

- a dissolved oxygen level in the range of 0-20 mg/L and 0-200 % saturation;
- a salinity in range 0-40 ppt; and
- a temperature of 0-45 degree Celsius

A membrane electrode with automatic temperature compensation complete with a cable was installed.

#### **Turbidity Measurement Instrument**

A portable and weatherproof turbidity meter (HACH model 2100Q) was used during impact monitoring. It has a photoelectric sensor capable of measuring turbidity between 0-1000 NTU. Response of the sensor was checked with certified standard Turbidity solutions before the start of measurement.

### For Water Sampling and Sample Analysis

In-situ monitoring was carried out at three depths: 1 meter below water surface, at mid-depth and 1 meter above the seabed. At each sampling depth, duplicate readings of dissolved oxygen content and turbidity were taken. The probes were retrieved out of the water after first measurement and then redeployed for the second measurement. The difference between the two readings of each set was more than 25% of the value of the first reading while a third measurement would be conducted to ensure data precision.

#### **Water Sampler**

A water sampler comprising a transparent PVC cylinder, with a capacity of not less than 2 liters, was lowered into the water body at the predetermined depth. The both opening ends of the sampler were then closed accordingly by dead weight and water samples were collected.

#### **Water Container**

The sample container, made by high-density polythene, was rinsed with a portion of the water sample. The water sample was then transferred to the container, labeled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4°C. The water samples were then delivered to a local HOKLAS-accredited laboratory (Environmental Laboratory, ETS-Testconsult Ltd, HOKLAS Registration No. 022) on the same day for analysis.



The summary of testing method of testing parameter as recommended by EIA or required by EPD, with the QA/QC results in accordance with the requirement of HOKLAS or international accredited scheme is shown in Table 5.2. For the QA/QC procedures, one QC sample, one duplicate sample and one sample spike of every batch of 20 samples were analysis. The QA/QC results are summarized in Appendix K.

Table 5.2 Summary of testing procedure

Laboratory Analysis	Testing Procedure	Detection Limit
Total suspended solids	In house method based on APHA 19 <sup>th</sup> ed 2540D	1.0 mg/L

### In-situ measurement

All in-situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use. Responses of sensors and electrodes were checked with certified standard solutions before each use. Wet bulb calibration for a DO meter was carried out before the start of measurement.

At each measurement/sampling depth, two consecutive measurements of dissolved oxygen (DO), dissolved oxygen saturation (DOS), turbidity and salinity were taken. For turbidity measurement, the sample was collected by using sampler and then transferred to the cell. The reading of turbidity of the sample was directly recorded from the Turbidimeter (HACH 2100Q) after inserting the cell to the Turbidimeter. For DO, DOS and Salinity, measurements were conducted three days per week at both mid-ebb and mid-flood tides at three depths (i.e. 1m below surface, mid depth and 1m from seabed). The duplicate measurements were averaged if the difference was not greater than 25%. If the difference is greater than 25%, repeat measurement will be required to be carried out.

Table 5.3 shows the equipment used for in-situ monitoring of water quality. The calibration certificates are attached in Appendix C1.

Table 5.3 Details of Marine Water Quality Monitoring Equipment (In-site measurement)

Parameter	Model	Date of Calibration	Due Date	Equipment No.
Coordinate of Monitoring stations	Garmin eTrex 10	-----	-----	ET/EW/005/04
Dissolved Oxygen (Saturation), Temperature, Salinity	YSI Dissolved Oxygen, Salinity & Temperature Meter, YSI Pro 2030	28/04/14	27/07/14	ET/EW/008/004 *
Turbidity	HACH Model 2100Q Turbid Meter	07/04/14	06/07/14	ET/0505/010 *
Water Depth	Speedtech SM-5	-----	-----	ET/EW/002/06

Remark:(\*) indicates the instrument should be calibrated on use.

## 5.5 Action and Limit Levels

The water quality criteria, namely Action and Limit (A/L) levels are presented in the table below.

Table 5.4 Water Quality Action and Limit Levels

Parameter	Action Level	Limit Level
DO (mg/L)	<u>Surface &amp; Middle</u> <4.78 mg/L (5%-ile of baseline data) <u>Bottom</u> <4.16 mg/L (5%-ile of baseline data)	<u>Surface &amp; Middle</u> <4.00 mg/L (1%-ile of baseline data) <u>Bottom</u> <2.00 mg/L
SS (mg/L) (Depth-averaged)	>120% of the upstream control station's SS at the same tide on the same day	>130% of the upstream control station's SS at the same tide on the same day
Turbidity (NTU) (Depth-averaged)	>120% of the upstream control station's turbidity at the same tide on the same day	>130% of the upstream control station's turbidity at the same tide on the same day



## 5.6 Event and Action Plan

Please refer to the Appendix F for details.

## 5.7 Monitoring Duration and Period in this reporting month

Table 5.5 is the time schedule for the marine water quality monitoring events that were conducted in this reporting period. Duration of marine water quality monitoring is detailed in Appendix C2.

Table 5.5 Time Schedule of Marine Water Quality Monitoring

May 2014						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

Remark (▼) : Marine water quality monitoring carried out by ET

## 5.8 Marine Water Quality Monitoring Results

The impact water quality measurement results are detailed in Appendix C2. Appendix C3 presents the water quality monitoring data and graphical presentations of monitoring results respectively.

The summary of marine water quality exceedances is shown in Table 5.6.

Table 5.6 Summary of Marine Water Quality Exceedances in this reporting month

Tide	Station	Exceedance Level	DO		Turbidity	SS	Total
			Surface & Middle	Bottom			
Mid-Ebb	TM-FM1	Action	0	0	0	0	0
		Limit	0	0	0	0	0
	TM-FM2	Action	0	0	0	0	0
		Limit	0	0	0	0	0
Mid-Flood	TM-FM1	Action	0	0	0	0	0
		Limit	0	0	0	0	0
	TM-FM2	Action	0	0	0	0	0
		Limit	0	0	0	0	0
Total		Action	0	0	0	0	0
		Limit	0	0	0	0	0

According to the summary of marine water monitoring results, no exceedances of Action and Limit levels were recorded for this reporting month.

## 6.0 Noise Monitoring

### 6.1 Monitoring Requirements

Noise monitoring was conducted at 2 designated monitoring stations as specified in the Sections 26.10 to 26.12 of the Particular Specification for good site practice.

The equipment, parameter, frequency, duration, methodology, calibration details, results and observations of the noise monitoring for the reporting month are presented in this section.



## 6.2 Monitoring Equipment

An Integrating Sound Level Meter was used for noise monitoring. It was a Type 1 sound level meter capable of giving a continuous readout of the noise level reading including equivalent continuous sound pressure level ( $L_{eq}$ ) and percentile sound pressure level ( $L_x$ ). It complies with International Electro Technical Commission Publications 651:1979 (Type1) and 804:1985 (Type1), and speed in m/s was used to monitor the wind speed.

Table 6.1 summarizes noise monitoring equipment model being used. A copy of the calibration certificate for noise meter and calibrator are attached in Appendix D1.

Table 6.1 Noise Monitoring Equipment

<i>Equipment</i>	<i>Model</i>
<i>Sound Level Meter</i>	<i>Rion NL-31 / Rion NL-52</i>
<i>Calibrator</i>	<i>Rion NC-73 / Castle GA607</i>

## 6.3 Monitoring Parameters, Duration and Frequency

Duration, frequencies and parameters of noise measurement are presented in Table 6.2.

Table 6.2 Duration, Frequencies and Parameters of Noise Monitoring

<i>Time period</i>	<i>Duration/min</i>	<i>Parameters</i>	<i>Frequency</i>
<i>Day-time: 0700-1900 hrs on normal weekday</i>	30	$L_{eq}$ , $L_{10}$ , $L_{90}$	Twice per week

## 6.4 Monitoring Locations and Period

Since Lands Dept did not approve to carry out noise monitoring at their own area where the noise monitoring stations TM-N1 and TM-N2 located due to the security, noise monitoring carried out at two noise monitoring stations TM-RN1 and TM-RN2 (refer to the figure 3 attached) from 18 December 2007.

The noise monitoring locations, TM-RN1 and TM-RN2 are shown in Figure 3. The noise measurement at TM-RN1 and TM-RN2 are façade measurement.

The noise-monitoring period of monitoring stations is summarized in Appendix D2.

## 6.5 Monitoring Procedures and Calibration Details

### Operation/Analysis Procedures

- The Sound Level Meter was set on a tripod at a height of 1.2m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - *Frequency weighting: A*
  - *Time weighting : Fast*
  - *Time measurement : 30 min*
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000HZ. If the difference in the calibration level before and after measurement was more than 1dB(A), the measurement would be considered invalid and repeat measurement would be required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with a portable wind meter.
- During the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Free Field correction to the measurements should be made. Correction factor of +3dB(A) should be made to the free Field measurements. Noise monitoring would be cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind gusts exceeding 10m/s.



### Maintenance and Calibration

- The microphone head of the sound level meter and calibrator are cleaned with soft cloth in quarterly intervals.
- The meter is sent to the supplier or HOKLAS laboratory to check and calibrated in yearly intervals.

## 6.6 Action and Limit Levels

The Action and Limit levels for noise levels derived as illustrated in Table 6.3.

Table 6.3 Action and Limit Levels for noise monitoring

<i>Time Period</i>	<i>Action *</i>	<i>Limit *</i>
0700-1900 hrs on normal weekdays	When one documented complaint is received	65 dB(A)

## 6.7 Event-Action Plans

Please refer to the Appendix F for details.

## 6.8 Results and Observation

The detail of the noise monitoring is provided in Appendix D2. Graphical presentation of the monitoring result for the reporting month is shown in Appendix D3.

Since no documented complaint on noise issue was received in this reporting month, no Action Level exceedance was recorded. Besides, no exceedance in Limit Level was recorded according to the result from Day-time noise monitoring.

The major sources of noise pollution observed in this reporting month were noise from the traveling dump trucks and from the operation of site machines.

## 7.0 ENVIRONMENTAL AUDIT

### 7.1 Weekly ET Site Inspection

Weekly site inspections were carried out by ET to monitor the timely implementation of proper environmental pollution control and mitigation measures for the Project. In this reporting month, four weekly site inspections were conducted on 08, 15, 22 and 29 May 2014. Summaries of key findings of weekly ET site inspections in this month are described in Table 7.1.

Table 7.1 Key Findings of Weekly ET Site Inspections in this reporting month

<i>Date</i>	<i>Key Findings</i>	<i>Action(s) Taken recommended by ET</i>	<i>Action(s) Taken by the Contractor during the site audit</i>	<i>Rectification Status by ET</i>
08 May 2014	No finding was recorded during the site inspection			
15 May 2014	No finding was recorded during the site inspection			
22 May 2014	The enclosure of tipping hall No.2 was damaged. (New item)	To repair the damaged part of tipping hall properly.	---	Follow-up
	Stagnant water was found accumulated inside the drip tray for a generator at work shop. (New item)	To drain off the stagnant water or apply pesticide to avoid mosquito breeding.	---	Follow-up
29 May 2014	The enclosure of tipping hall No.2 was damaged. (Previous item)	To repair the damaged part of tipping hall properly.	---	Follow-up
	Stagnant water was found accumulated inside the drip tray for a generator at work shop. (Previous item)	To drain off the stagnant water or apply pesticide to avoid mosquito breeding.	Stagnant water accumulated inside the drip tray for a generator at work shop was cleared.	Closed



## 7.2 Review of Environmental Monitoring Procedures

The monitoring works conducted by the ET were inspected internally on a regular basis. The following observations have been recorded for the monitoring works:

### **Air Quality Monitoring**

- The monitoring team recorded the observations around the monitoring stations within and outside of the construction site.
- The monitoring team recorded the temperature, air pressure and general weather condition on the monitoring day.

### **Water Quality Monitoring**

- The monitoring team recorded the observations around the monitoring stations, which might affect the results; and
- Major water pollution sources were identified and recorded.

### **Noise Monitoring**

- The monitoring team recorded the observations around the monitoring station, which might affect the results.
- Major noise sources were identified and recorded.

## 7.3 Status of Environmental Licensing and Permitting

All permits/licenses valid in this reporting month are summarized in Table 7.2.

Table 7.2 Summary of environmental licensing and permit status

Description	Permit No.	Valid Period		Section
		From	To	
Environmental Permit	EP-210/2005/B	08/04/13	---	Issued
Marine Dumping Permit	EP/MD/14-156	01/04/14	30/06/14	Approval for dumping 2,300,000 tons (approximately equal to 1,277,777 cu.m. bulked quantity) of Public Fill (Reclamation Materials) from Tseung Kwan O Area 137 Fill Bank and Tuen Mun Area 38 Fill Bank to designated dumping area at Guanghaiwan of Taishan
Chemical Waste Producer	5296-421-H3555-01	21/01/14	---	Spent battery containing heavy metals and spent lubricating oil
Effluent Discharge License	WT00018973-2014	23/05/14	31/05/19	Discharge of Industrial Trade Effluent arising from public fill reception facilities, screen and sedimentation tank
Billing Account for Waste Disposal	7018998	---	---	---

## 7.4 Implementation Status

### 7.4.1 Implementation Status of Environmental Mitigation Measures

An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in Appendix I. Most of the necessary mitigation measures were implemented properly.

### 7.4.2 Implementation Status of Event and Action Plan

No exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

Apart from this, there was no exceedance on noise and marine water monitoring parameters recorded in this monitoring month. Hence no further actions were required.

### 7.4.3 Implementation Status of Environmental Complaint, Notification of Summon and Successful Prosecution Handling

No complaint, notification of summon and prosecution with respect to environmental issues was received in this monitoring month.

A summary of environmental complaints, notifications of summons and successful prosecutions was given in Table 7.3.

Table 7.3 Summary of Environmental Complaints and Prosecutions

<i>Complaints logged</i>		<i>Summons served</i>		<i>Successful Prosecution</i>	
<i>May 2014</i>	<i>Cumulative</i>	<i>May 2014</i>	<i>Cumulative</i>	<i>May 2014</i>	<i>Cumulative</i>
0	0	0	0	0	0

## 8.0 LANDSCAPE AND VISUAL

Landscape and visual site audit was carried out on a weekly basis to monitor environmental issues in order to ensure that all mitigation measures were implemented timely and properly. The findings in this reporting month were:

- The maximum stockpiling height at the Fill Bank was limited to a maximum of +40 mPD;
- The Contractor hydroseeded the outer slopes of the Fill Bank as far as practicable;
- The Contractor removed the stockpile of public fill in a sequence to allow the outer hydroseeded to be removed later than other portions as far as practicable; and
- Lighting was set to minimize night-time glare.

## 9.0 WASTE MANAGEMENT

### 9.1 Summary of Waste disposed of in this month

The actual amounts of different types of waste disposed of by the activities of the Project in the month are shown in Table 9.1

Table 9.1 Actual amounts of Waste generated in this reporting month

<i>Waste Type</i>	<i>Actual Amount</i>	<i>Disposal Locations</i>
<i>Public Fill (m<sup>3</sup>)</i>	67	<i>Tuen Mun 38 Fill Bank</i>
<i>C&amp;D Waste (general refuse) (kg)</i>	0	<i>WENT Landfill</i>
<i>Chemical Waste (kg/L)</i>	0	<i>Collected by licensed collector</i>

### 9.2 Advice on the Solid and Liquid Waste Management Status

The Contractor should provide sufficient preventive measures during equipment maintenance works so as to avoid oil leakage on the ground. In the event of any oil leakage, the Contractor should clean up the polluted soil and handle all the materials used for this cleaning works as chemical waste.

The drain outlet of all the bunded areas should be plugged properly. Besides, pre-cast drip trays were provided for oil drums at several areas, such as workshop and chemical storage area. The Contractor should collect and dispose of any stagnant water accumulated in the concrete bunding and drip trays and handle them as chemical waste.

The Contractor should use suitable containers with proper labels to store chemical wastes in accordance with Code of Practice on the Packaging, Labeling and Storage of Chemical Waste. The Contractor should also advise their workers of the proper procedures in handling the chemical waste. All the trip tickets for chemical waste disposal should be properly kept in the site office.

The Contractor was reminded to increase the frequency of inspection and cleaning of the site drainage system, including permanent desilting chambers, desilting facilities, oil interceptor bypass tank and all the trapezoidal channels. Moreover, the Contractor should apply approved pesticides in the stagnant water ponds.





All the runoff from the parking area should be pumped to the desilting facilities and oil interceptors to remove suspended solids and oil & grease prior to discharge.

## 10.0 ENVIRONMENTAL NON-CONFORMANCE

### 10.1 Summary of air quality, noise and marine water quality

No exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

According to the summary of marine water monitoring results, no exceedance of Action and Limit levels was recorded for this reporting month.

The noise level measured at the monitoring station complied with the Limit Level of 65dB(A). No complaint was received regarding noise issue in this reporting month.

### 10.2 Summary of Environmental Complaints

No complaint was occurred in this reporting month.

### 10.3 Summary of Notification of Summons and Prosecution

There was no notification of summon and prosecution respect to environmental issues registered in this reporting month.

## 11.0 CONCLUSIONS AND RECOMMENDATIONS

### Conclusions

Impact monitoring of air quality, noise and water quality were carried out at designated locations in this reporting month.

According to the summary of air monitoring results, no exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

According to the summary of marine water monitoring results, no exceedance of Action and Limit levels was recorded in this reporting month.

The noise level measured at the monitoring station complied with the Limit Level of 65dB(A). No complaint was received regarding noise issue in this reporting month.

According to the weekly site inspections carried out in this reporting month, the Contractor generally implemented sufficient dust mitigation measures, including operation of the mist spraying systems and automatic wheel washing facilities, dampening of haul roads and stockpiling areas.

No complaint, prosecution or notification of summons was received in this reporting month.

### Recommendations

According to the environmental site inspections performed in the reporting month, the following recommendations were provided:

#### **Air Quality**

- Ensure the frequency of water spraying on haul roads, unloading areas and stockpiles to be sufficient to suppress the dust sources;
- Provide proper maintenance for the powered mechanical equipment and barges to avoid emission of dark smoke;
- Provide water spraying onto the truckloads during inspection of fill material;



- Conduct road sweeping on all paved haul roads and public roads especially outside and near the site egress by the road sweeper. Undertake water spraying on stockpiling area by water bowsers;
- Erect adequate speed limit signs to advise the truck drivers of the speed limit;
- Operate mist spraying systems and automatic water sprinklers in the Fill Bank;
- Implement the dust mitigation measures for the construction activities;
- Designate proper haul roads to ensure effective water spraying; and
- Ensure all vehicles to be washed before leaving the site egress by provision, operation and maintenance of automatic wheel washing facilities.

#### **Noise**

- Conduct noisy activities at a farther location from the NSRs.

#### **Water Quality**

- Maintain the drainage system, including the trapezoidal channels and permanent desilting chambers regularly; and
- Remove the stagnant water or provide approved pesticides for the stagnant water in the permanent desilting chambers, if any.

#### **Chemical and Waste Management**

- Remove waste materials from the site to avoid accumulation regularly;
- Handle and store chemical wastes properly;
- Remove unwanted material in the existing stockpiles and avoid further dumping of such material;
- Provide and maintain sufficient drip trays for diesel drums, chemical containers, chemical waste storage drums and diesel operated generator set;
- Maintain good housekeeping at the workshop area;
- Ensure sufficient tarpaulin sheets are provided to cover drip trays; and
- Avoid soil being polluted during oil filling and equipment maintenance; hence, properly remove and store the contaminated soil, if any.

#### **Landscape and Visual**

- Provide hydroseeding on the exposed slopes, on which the final profile has been formed;
- Erect all the site hoarding/chaining fences in accordance with agreed design at proper location; and
- Maintain the hydroseeded slopes properly.

## **12.0 FUTURE KEY ISSUES**

Based on the site inspections and forecast of engineering works in the coming month, key issues to be considered are as follows:

- Dust generation from activities on site, such as vehicular movements along unpaved area and rock crushing activities;
- Noise impact from operating equipment and machinery on site and
- Wastewater and surface runoff from the site discharged into nearby water body.


- END OF REPORT -



## **Appendix A**

### **Project Organization Chart**

# ORGAINZATIONAL CHART OF ENVIRONMENTAL MANAGEMENT TEAM

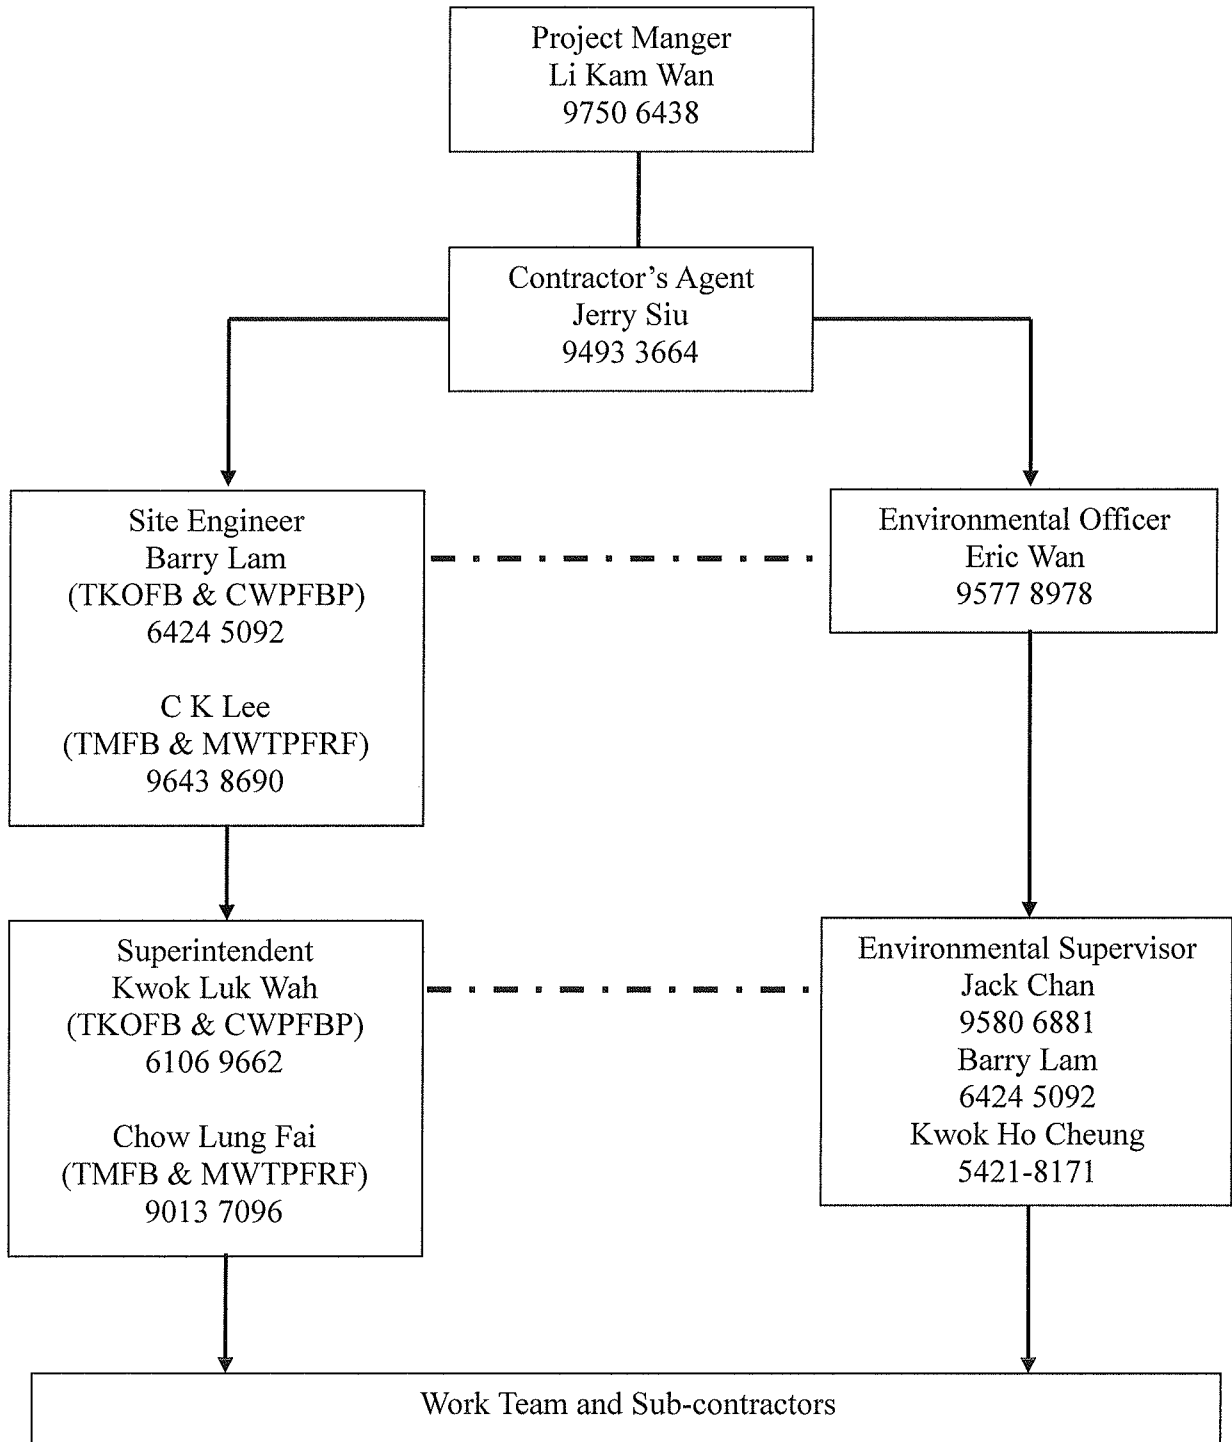

Key:


→ : Line of Authority

- . - . : Line of Communication



## **Appendix B1**

### **Calibration Certificates for Impact Air Quality Monitoring Equipments**



東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED


8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong  
Tel : 2695 8318 E-mail : etl@ets-testconsult.com  
Fax : 2695 3944 Web site : www.ets-testconsult.com

**Calibration Report**  
of  
**High Volume Air Sampler**

Manufacturer : Graseby GMW Date of Calibration : 14 March 2014  
Serial No. : 10347 ( ET / EA / 003 / 06) Calibration Due Date : 13 May 2014  
Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results	Flow recorder reading (cfm)	58	52	44	37	29
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.59	1.40	1.21	0.97	0.76
	Pressure : 770.31 mm Hg	Temp. : 294 K				

**Sampler 10347 Calibration Curve**  
Site: Tuen Mun 38 (TM-A1)

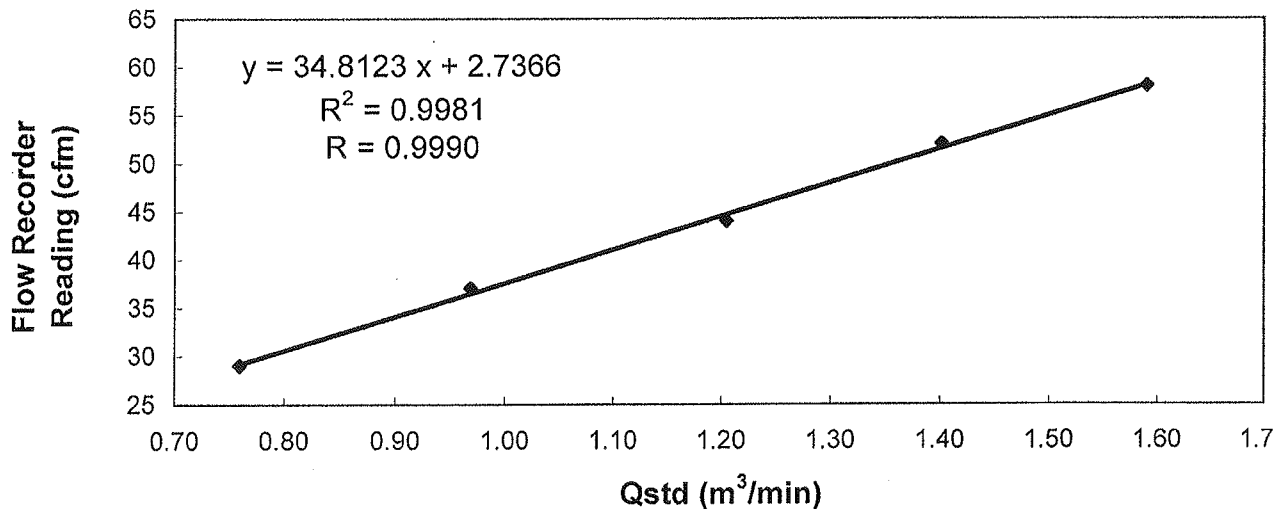

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\* / unacceptable\* for use.

Calibrated by : MAK Kei Wai  
MAK, Kei Wai  
(Assistant Supervisor)

Approved by : LAW Sau Yee  
LAW, Sau Yee  
(Senior Environmental Officer)



東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED


8/F, Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong  
Tel : 2695 8318 E-mail : etl@ets-testconsult.com  
Fax : 2695 3944 Web site : www.ets-testconsult.com

**Calibration Report**  
of  
**High Volume Air Sampler**

Manufacturer : Graseby GMW Date of Calibration : 08 May 2014  
Serial No. : 10347 (ET / EA / 003 / 06) Calibration Due Date : 07 July 2014  
Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results	Flow recorder reading (cfm)	58	53	44	37	28
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.60	1.40	1.21	0.97	0.78
	Pressure : 765.81 mm Hg	Temp. : 293 K				

**Sampler 10347 Calibration Curve**  
Site: Tuen Mun 38 (TM-A1)

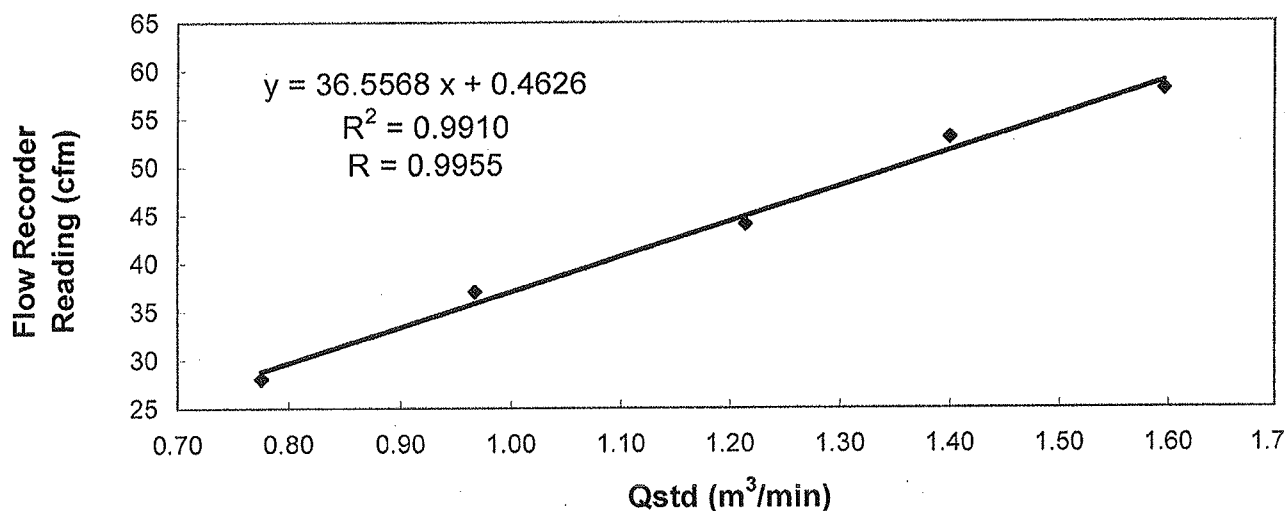

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / does not comply\* with the specified requirements and is deemed acceptable\* / unacceptable\* for use.

Calibrated by : MAK Kei Wai  
MAK, Kei Wai  
(Assistant Supervisor)

Approved by : LAW Sau Yee  
LAW, Sau Yee  
(Senior Environmental Officer)



東業德勤測試顧問有限公司

ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong

Tel : 2695 8318

E-mail : etl@ets-testconsult.com

Fax : 2695 3944

Web site : www.ets-testconsult.com

**Calibration Report**  
**of**  
**High Volume Air Sampler**


Manufacturer : Graseby GMW Date of Calibration : 08 March 2014

Serial No. : 9864 ( ET / EA / 003 / 19 ) Calibration Due Date : 07 May 2014

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results	Flow recorder reading (cfm)	48	42	36	29	25
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.75	1.55	1.38	1.09	0.84
	Pressure : 763.56 mm Hg	Temp. : 291 K				

**Sampler 9864 Calibration Curve**  
**Site: Tuen Mun (TM-RA2)**

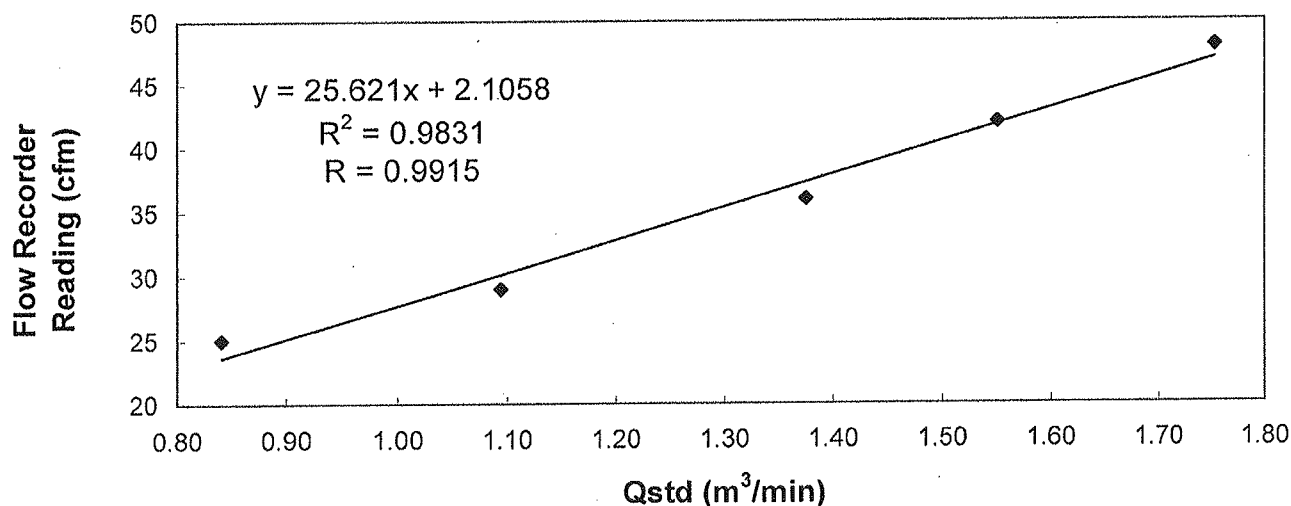

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / ~~does not comply\*~~ with the specified requirements and is deemed acceptable\* / unacceptable\* for use.

Calibrated by : MAK, Kei Wai  
MAK, Kei Wai  
(Assistant Supervisor)

Checked by : LAW, Sau Yee  
LAW, Sau Yee  
(Senior Environmental Officer)

- END OF REPORT -





東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED


8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong  
Tel : 2695 8318 E-mail : etl@ets-testconsult.com  
Fax : 2695 3944 Web site : www.ets-testconsult.com

**Calibration Report**  
of  
**High Volume Air Sampler**

Manufacturer : Graseby GMW Date of Calibration : 08 May 2014  
Serial No. : 9864 (ET / EA / 003 / 19) Calibration Due Date : 07 July 2014  
Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results	Flow recorder reading (cfm)	48	42	37	30	26
	Qstd (Actual flow rate, m <sup>3</sup> /min)	1.74	1.55	1.38	1.09	0.84
	Pressure : 765.81 mm Hg	Temp. : 293 K				

**Sampler 9864 Calibration Curve**  
Site: Tuen Mun (TM-RA2)

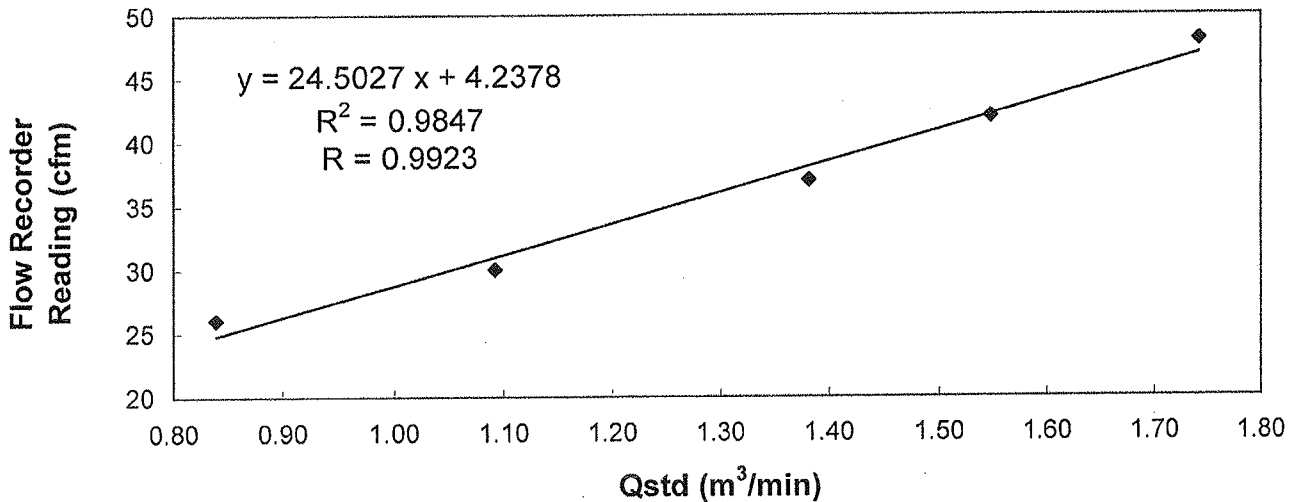

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies\* / ~~does not comply\*~~ with the specified requirements and is deemed acceptable\* / unacceptable\* for use.

Calibrated by : MAK, Kei Wai  
MAK, Kei Wai  
(Assistant Supervisor)

Checked by : LAW, Sau Yee  
LAW, Sau Yee  
(Senior Environmental Officer)



TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE.  
 VILLAGE OF CLEVELAND, OH 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX  
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT  
 ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - May 13, 2013 Rootsometer S/N 0438320 Ta (K) - 296  
 Operator Tisch Orifice I.D. - 2511 Pa (mm) - 753.11

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER	ORFICE
					DIFF Hg (mm)	DIFF H2O (in.)
1	NA	NA	1.00	1.4400	3.2	2.00
2	NA	NA	1.00	1.0110	6.4	4.00
3	NA	NA	1.00	0.9030	7.9	5.00
4	NA	NA	1.00	0.8630	8.8	5.50
5	NA	NA	1.00	0.7110	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9934	0.6898	1.4125	0.9957	0.6915	0.8866
0.9892	0.9784	1.9976	0.9915	0.9807	1.2539
0.9871	1.0931	2.2334	0.9894	1.0957	1.4019
0.9860	1.1425	2.3424	0.9883	1.1452	1.4703
0.9808	1.3794	2.8251	0.9831	1.3827	1.7732
Qstd slope (m) = 2.05038			Qa slope (m) = 1.28391		
intercept (b) = -0.00442			intercept (b) = -0.00277		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		

y axis =  $\sqrt{H_2O(Pa/760)(298/Ta)}$

y axis =  $\sqrt{H_2O(Ta/Pa)}$

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)  
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]  
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd =  $1/m\{[\sqrt{H_2O(Pa/760)(298/Ta)}] - b\}$   
 Qa =  $1/m\{[\sqrt{H_2O(Ta/Pa)}] - b\}$



## **Appendix B2**

### **Impact Air Quality Monitoring Results**



## Summary of 24-hr TSP Monitoring Results

Monitoring Station : TM-A1

Date	Start Time	Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min.)		Average (m <sup>3</sup> /min.)	Filter Weight (g)		Conc. (µg/m <sup>3</sup> )
		Date	Time	Initial	Final		Initial	Final		Initial	Final	
05/05/14	08:00	06/05/14	08:00	16092.86	16116.86	24.00	0.8981	0.8981	0.8981	2.7412	2.8821	109
11/05/14	08:00	12/05/14	08:00	16119.86	16143.86	24.00	0.8035	0.8035	0.8035	2.7363	2.8745	119
17/05/14	13:00	18/05/14	13:00	16147.86	16171.86	24.00	0.8035	0.8035	0.8035	2.7611	2.8598	85
23/05/14	09:00	24/05/14	09:00	16173.86	16197.86	24.00	0.8035	0.8035	0.8035	2.7734	2.8741	87
29/05/14	10:00	30/05/14	10:00	16201.86	16225.86	24.00	0.8035	0.8035	0.8035	2.7721	2.8746	89

Monitoring Station : TM-RA2

Date	Start Time	Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min.)		Average (m <sup>3</sup> /min.)	Filter Weight (g)		Conc. (µg/m <sup>3</sup> )
		Date	Time	Initial	Final		Initial	Final		Initial	Final	
05/05/14	08:00	06/05/14	08:00	2952.05	2976.05	24.00	1.2449	1.2449	1.2449	2.7381	3.0157	155
11/05/14	08:00	12/05/14	08:00	2979.05	3003.05	24.00	1.2146	1.2146	1.2146	2.7410	3.0175	158
17/05/14	13:00	18/05/14	13:00	3007.05	3031.05	24.00	1.2146	1.2146	1.2146	2.7394	2.9823	139
23/05/14	09:00	24/05/14	09:00	3033.05	3057.05	24.00	1.2146	1.2146	1.2146	2.7529	2.9972	140
29/05/14	10:00	30/05/14	10:00	3061.05	3085.05	24.00	1.2146	1.2146	1.2146	2.7705	3.0103	137



## Summary of 1-hr TSP Monitoring Results

Monitoring Station : TM-A1

Date	Time		Elapse Time		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min.)		Average (m <sup>3</sup> /min.)	Filter Weight (g)		Conc. (µg/m <sup>3</sup> )
	Start	Finish	Initial	Final		Initial	Final		Initial	Final	
03/05/14	10:00	11:00	16090.86	16091.86	1.00	0.8981	0.8981	0.8981	2.7484	2.7605	225
03/05/14	11:24	12:24	16091.86	16092.86	1.00	0.8981	0.8981	0.8981	2.7398	2.7517	221
08/05/14	08:45	09:45	16116.86	16117.86	1.00	0.8035	0.8035	0.8035	2.7394	2.7495	210
08/05/14	13:00	14:00	16117.86	16118.86	1.00	0.8035	0.8035	0.8035	2.7443	2.7540	201
10/05/14	08:30	09:30	16118.86	16119.86	1.00	0.8035	0.8035	0.8035	2.7413	2.7536	255
13/05/14	09:35	10:35	16143.86	16144.86	1.00	0.8035	0.8035	0.8035	2.7597	2.7677	166
13/05/14	10:40	11:40	16144.86	16145.86	1.00	0.8035	0.8035	0.8035	2.7493	2.7580	180
15/05/14	13:00	14:00	16145.86	16146.86	1.00	0.8035	0.8035	0.8035	2.7368	2.7460	191
17/05/14	09:35	10:35	16146.86	16147.86	1.00	0.8035	0.8035	0.8035	2.7539	2.7610	147
20/05/14	09:40	10:40	16171.86	16172.86	1.00	0.8035	0.8035	0.8035	2.7634	2.7704	145
22/05/14	08:00	09:00	16172.86	16173.86	1.00	0.8035	0.8035	0.8035	2.7492	2.7567	156
24/05/14	09:05	10:05	16197.86	16198.86	1.00	0.8035	0.8035	0.8035	2.7423	2.7530	222
24/05/14	13:00	14:00	16198.86	16199.86	1.00	0.8035	0.8035	0.8035	2.7391	2.7489	203
27/05/14	08:55	09:55	16199.86	16200.86	1.00	0.8035	0.8035	0.8035	2.7392	2.7461	143
29/05/14	08:40	09:40	16200.86	16201.86	1.00	0.8035	0.8035	0.8035	2.7682	2.7756	153
31/05/14	10:10	11:10	16225.86	16226.86	1.00	0.8035	0.8035	0.8035	2.7704	2.7790	178

Monitoring Station : TM-RA2


Date	Time		Elapse Time		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min.)		Average (m <sup>3</sup> /min.)	Filter Weight (g)		Conc. (µg/m <sup>3</sup> )
	Start	Finish	Initial	Final		Initial	Final		Initial	Final	
03/05/14	10:07	11:07	2950.05	2951.05	1.00	1.2449	1.2449	1.2449	2.7398	2.7589	256
03/05/14	11:30	12:30	2951.05	2952.05	1.00	1.2449	1.2449	1.2449	2.7412	2.7597	248
08/05/14	08:50	09:50	2976.05	2977.05	1.00	1.2146	1.2146	1.2146	2.7308	2.7516	285
08/05/14	13:00	14:00	2977.05	2978.05	1.00	1.2146	1.2146	1.2146	2.7530	2.7745	295
10/05/14	08:35	09:35	2978.05	2979.05	1.00	1.2146	1.2146	1.2146	2.7403	2.7582	246
13/05/14	09:40	10:40	3003.05	3004.05	1.00	1.2146	1.2146	1.2146	2.7601	2.7802	276
13/05/14	10:45	11:45	3004.05	3005.05	1.00	1.2146	1.2146	1.2146	2.7606	2.7816	288
15/05/14	13:00	14:00	3005.05	3006.05	1.00	1.2146	1.2146	1.2146	2.7297	2.7505	285
17/05/14	09:40	10:40	3006.05	3007.05	1.00	1.2146	1.2146	1.2146	2.7463	2.7661	272
20/05/14	09:45	10:45	3031.05	3032.05	1.00	1.2146	1.2146	1.2146	2.7558	2.7738	247
22/05/14	08:00	09:00	3032.05	3033.05	1.00	1.2146	1.2146	1.2146	2.7399	2.7590	262
24/05/14	09:10	10:10	3057.05	3058.05	1.00	1.2146	1.2146	1.2146	2.7325	2.7449	170
24/05/14	13:05	14:05	3058.05	3059.05	1.00	1.2146	1.2146	1.2146	2.7412	2.7527	158
27/05/14	09:00	10:00	3059.05	3060.05	1.00	1.2146	1.2146	1.2146	2.7433	2.7617	252
29/05/14	08:44	09:44	3060.05	3061.05	1.00	1.2146	1.2146	1.2146	2.7593	2.7783	261
31/05/14	10:20	11:20	3085.05	3086.05	1.00	1.2146	1.2146	1.2146	2.7713	2.7896	251




## **Appendix B3**

### **Graphical Plots of Impact Air Quality Monitoring Data**

**24-hour TSP level at TM-A1**

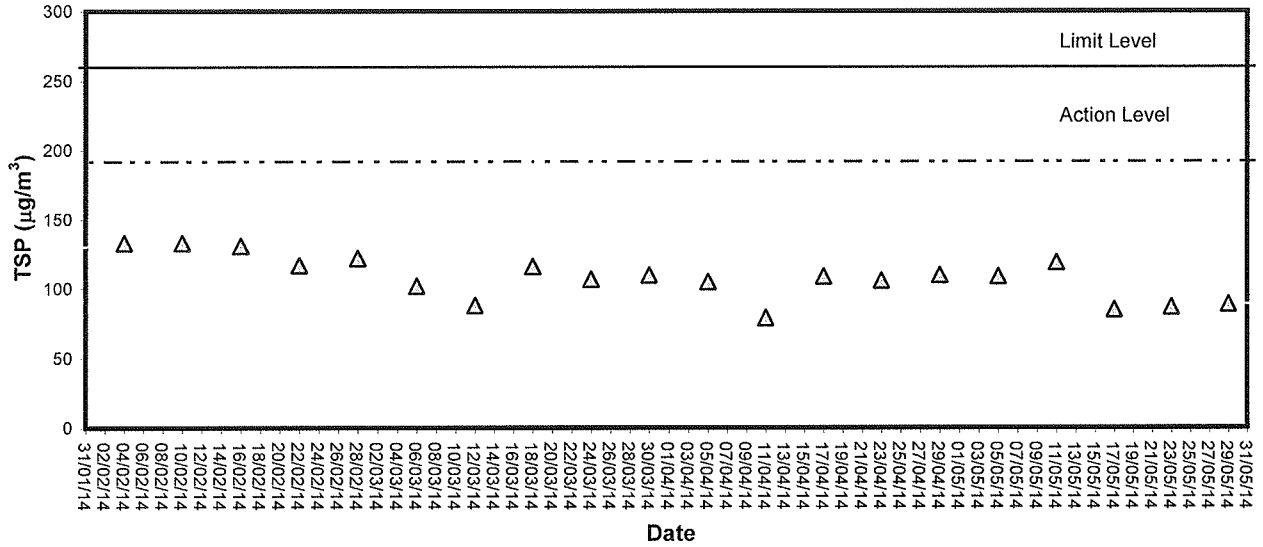


**24-hour TSP level at TM-RA2**

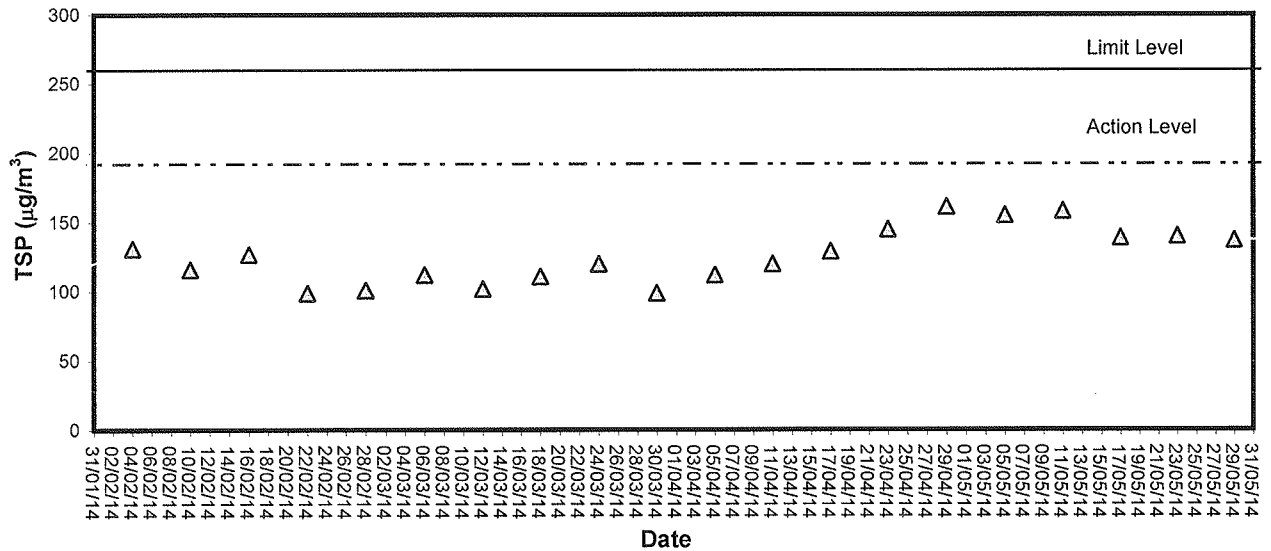




### 1-hour TSP level at TM-A1

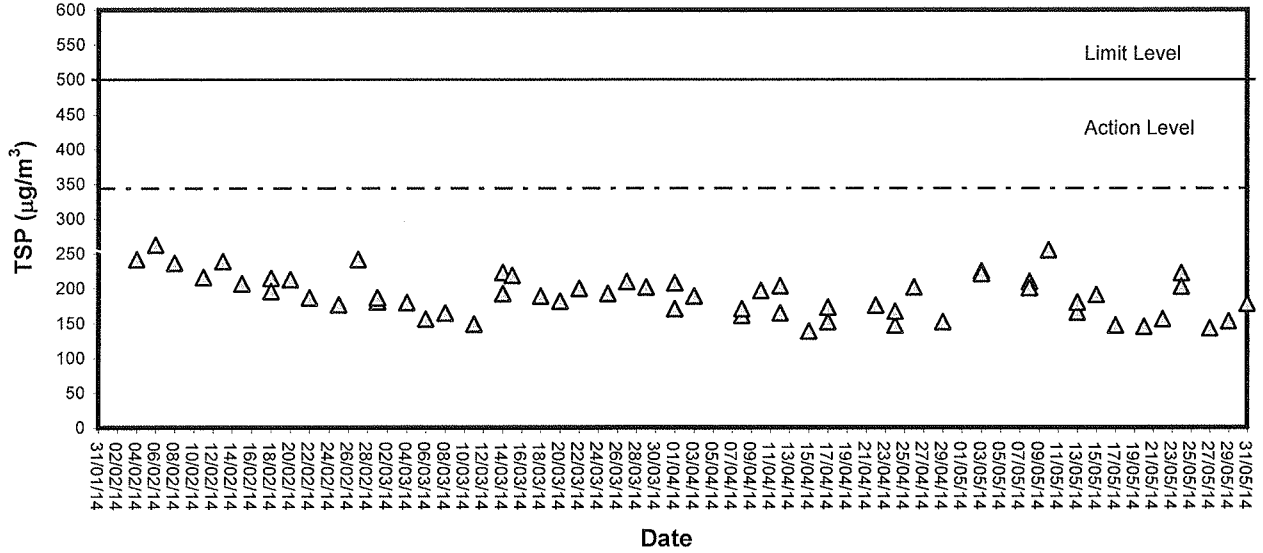

### 1-hour TSP level at TM-RA2

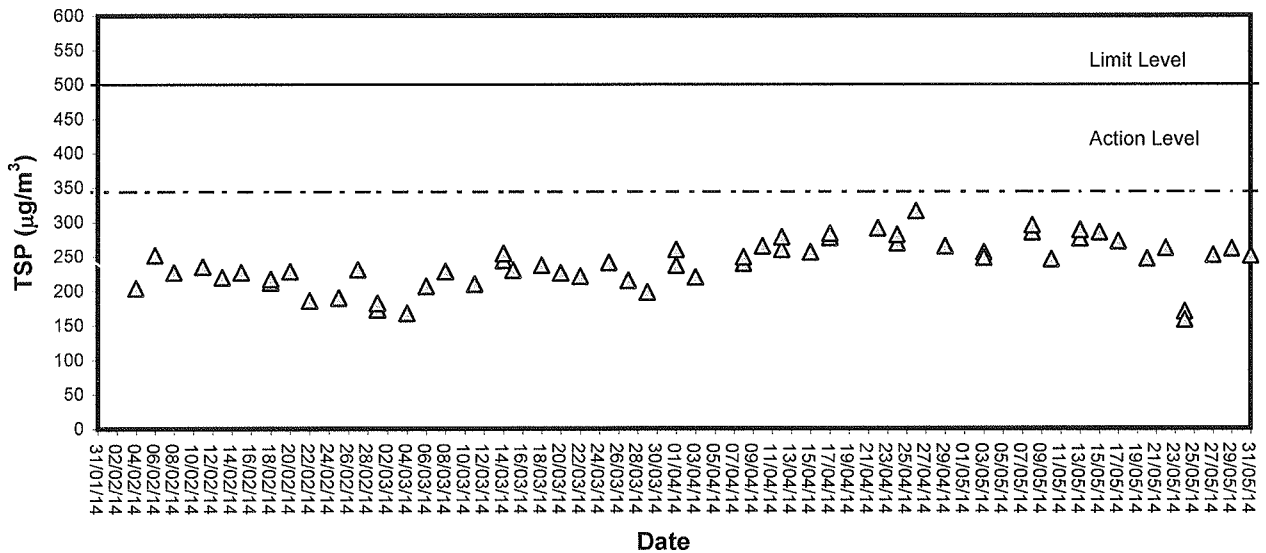





## **Appendix C1**

### **Calibration Certificates for Impact Marine Water Quality Monitoring Equipments**



### Internal Calibration Report of Dissolved Oxygen Meter

Equipment Ref. No. : <u>ET/EW/008/004</u>	Manufacturer : <u>YSI</u>
Model No. : <u>Pro 2030</u>	Serial No. : <u>10F 101978</u>
Date of Calibration : <u>28/04/2014</u>	Calibration Due Date : <u>27/07/2014</u>

#### Temperature Verification

Ref. No. of Reference Thermometer : ET/0521/008

Ref. No. of Water Bath : ---

		Temperature (°C)		
Reference Thermometer reading	Measured	20.1	Corrected	19.7
DO Meter reading	Measured	19.6	Difference	0.1

#### Standardization of sodium thiosulphate ( $Na_2S_2O_3$ ) solution

Reagent No. of $Na_2S_2O_3$ titrant	<u>CPE/012/4.5/001/8</u>	Reagent No. of 0.025N $K_2Cr_2O_7$	<u>CPE/012/4.4/001/26</u>
		Trial 1	Trial 2
Initial Vol. of $Na_2S_2O_3$ (ml)		0.00	10.20
Final Vol. of $Na_2S_2O_3$ (ml)		10.20	20.45
Vol. of $Na_2S_2O_3$ used (ml)		10.20	10.25
Normality of $Na_2S_2O_3$ solution (N)		0.02451	0.02439
Average Normality (N) of $Na_2S_2O_3$ solution (N)		0.02445	
Acceptance criteria, Deviation		Less than $\pm 0.001N$	

Calculation: Normality of  $Na_2S_2O_3$ ,  $N = 0.25 / ml Na_2S_2O_3$  used

#### Linearity Checking

##### Determination of dissolved oxygen content by Winkler Titration \*

Purging Time (min)	2		5		10	
	1	2	1	2	1	2
Trial						
Initial Vol. of $Na_2S_2O_3$ (ml)	0.00	12.00	24.00	0.00	8.10	12.90
Final Vol. of $Na_2S_2O_3$ (ml)	12.00	24.00	32.00	8.10	12.90	17.60
Vol. (V) of $Na_2S_2O_3$ used (ml)	12.00	12.00	8.00	8.10	4.80	4.70
Dissolved Oxygen (DO), mg/L	7.88	7.88	5.25	5.32	3.15	3.08
Acceptance criteria, Deviation	Less than + 0.3mg/L		Less than + 0.3mg/L		Less than + 0.3mg/L	

Calculation:  $DO (mg/L) = V \times N \times 8000/298$

Purging time, min	DO meter reading, mg/L			Winkler Titration result *, mg/L			Difference (%) of DO Content
	1	2	Average	1	2	Average	
2	7.75	7.71	7.73	7.88	7.88	7.88	1.92
5	5.39	5.41	5.40	5.25	5.32	5.29	2.06
10	3.14	3.11	3.13	3.15	3.08	3.12	0.32
Linear regression coefficient				0.9977			



### Internal Calibration Report of Dissolved Oxygen Meter

**Zero Point Checking**

DO meter reading, mg/L	0.00
------------------------	------

**Salinity Checking**

Reagent No. of NaCl (10ppt)	CPE/012/4.7/002/19	Reagent No. of NaCl (30ppt)	CPE/012/4.8/002/19
-----------------------------	--------------------	-----------------------------	--------------------

**Determination of dissolved oxygen content by Winkler Titration \*\***

Salinity (ppt)	10		30	
Trial	1	2	1	2
Initial Vol. of Na <sub>2</sub> S <sub>2</sub> O <sub>3</sub> (ml)	0.00	11.90	23.70	34.20
Final Vol. of Na <sub>2</sub> S <sub>2</sub> O <sub>3</sub> (ml)	11.90	23.70	34.20	44.80
Vol. (V) of Na <sub>2</sub> S <sub>2</sub> O <sub>3</sub> used (ml)	11.90	11.80	10.50	10.60
Dissolved Oxygen (DO), mg/L	7.81	7.75	6.89	6.96
Acceptance criteria, Deviation	Less than + 0.3mg/L		Less than + 0.3mg/L	

Calculation:  $DO \text{ (mg/L)} = V \times N \times 8000/298$

Salinity (ppt)	DO meter reading, mg/L			Winkler Titration result**, mg/L			Difference (%) of DO Content
	1	2	Average	1	2	Average	
10	7.87	7.82	7.85	7.81	7.75	7.78	0.90
30	7.12	7.18	7.15	6.89	6.96	6.93	3.13

**Acceptance Criteria**

- (1) Differenc between temperature readings from temperature sensor of DO probe and reference thermometer : < 0.5 °C
- (2) Linear regression coefficient : >0.99
- (3) Zero checking: 0.0mg/L
- (4) Difference (%) of DO content from the meter reading and by winkler titration : within ± 5%

The equipment complies # / does-not-comply # with the specified requirements and is deemed acceptable # / unacceptable # for use.

# Delete as appropriate

Calibrated by

:

Approved by :



## Performance Check of Salinity Meter

Equipment Ref. No. : ET/EW/008/004      Manufacturer : YSI  
Model No. : Pro 2030      Serial No. : 10F 101978  
Date of Calibration : 28/04/2014      Due Date : 27/07/2014

Ref. No. of Salinity Standard used (30ppt)

S/001/5

Salinity Standard (ppt)	Measured Salinity (ppt)	Difference * (%)
30.0	31.5	5.00


(\* ) Difference (%) = (Measured Salinity – Salinity Standard value) / Salinity Standard value x 100

Acceptance Criteria

Difference : -10 % to 10 %

The salinity meter complies \* / ~~does not comply~~ \* with the specified requirements and is deemed acceptable \* / ~~unacceptable~~ \* for use. Measurements are traceable to national standards.

Checked by : 

Approved by : 



## Performance Check of Turbidity Meter

Equipment Ref. No. : ET/0505/010 Manufacturer : HACH

Model No. : 2100Q Serial No. : 11110 C 014260

Date of Calibration : 07/04/2014 Due Date : 06/07/2014

Theoretical Value of Turbidity Standard (NTU)	Measured Value (NTU)	Difference % *
20	19.5	-2.50
100	103	3.00
800	792	-1.00

(\*) Difference = (Measured Value – Theoretical Value) / Theoretical Value x 100

Acceptance Criteria

Difference : -5 % to 5 %

The turbidity meter complies \* / ~~does not comply~~ \* with the specified requirements and is deemed acceptable \* / ~~unacceptable~~ \* for use. Measurements are traceable to national standards.

Prepared by : 

Checked by : 



## **Appendix C2**

### **Impact Marine Water Quality Monitoring Results**

# Mid-Flood Tide



東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED

## Monitoring Station : TM-FC1

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)		Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Depth-average
03/05/14	0911-0930	24/Fne	Surface	23.9	26.4	26.5	5.98	5.98	5.93	81.7	81.7	3.86	3.88	4.8	4.9	5.0	
					26.5	26.8	5.97	5.88	81.6	80.5	3.89	3.99	5.0	5.1			
					26.8	26.9	5.87	5.84	80.3	80.0	3.98	4.05	5.2	5.1			
08/05/14	1439-1500	22/Cloudy	Surface	23.6	26.8	26.9	5.85	5.84	5.84	80.1	80.0	4.05	4.05	5.2	5.1	4.9	
					26.9	27.2	5.83	5.41	79.8	75.0	4.04	3.70	5.0	4.7			
					27.2	27.4	5.40	5.22	74.8	72.2	3.70	3.92	4.8	4.9			
10/05/14	1638-1700	22/Cloudy	Surface	21.7	27.3	27.4	5.20	5.20	5.49	71.8	71.3	3.93	3.92	5.2	5.1	5.2	
					27.4	27.5	5.23	5.08	72.6	70.4	3.90	4.09	5.0	5.1			
					27.5	27.0	5.07	5.57	69.8	76.1	4.07	4.03	5.0	5.1			
13/05/14	1843-1900	25/Cloudy	Surface	23.5	27.5	27.5	5.09	5.74	5.74	70.9	76.7	4.10	3.94	5.2	4.9	4.8	
					27.5	27.1	5.56	5.96	75.9	79.6	4.10	3.70	5.2	4.6			
					27.0	27.0	5.58	5.42	76.2	73.8	4.04	4.10	5.0	4.6			
15/05/14	1914-1930	27/Cloudy	Surface	25.6	27.1	27.1	5.41	5.25	5.25	73.7	71.3	4.10	3.03	4.8	4.1	4.6	
					27.2	27.2	5.19	5.95	71.1	80.4	4.10	3.95	5.2	4.9			
					21.1	21.1	5.21	6.03	71.4	80.6	4.08	3.52	5.4	4.8			
17/05/14	0830-0845	25/Rainy	Surface	25.2	21.1	21.1	6.07	6.03	5.79	80.3	81.1	3.51	4.92	4.8	6.1	6.6	
					21.1	22.3	6.11	5.96	80.8	74.9	3.52	5.55	4.8	6.7			
					22.2	22.5	5.97	5.74	79.7	73.0	3.71	5.66	4.8	6.9			
20/05/14	1041-1100	25/Cloudy	Surface	25.1	22.3	22.3	5.95	5.41	5.41	79.4	73.0	3.68	5.66	4.4	5.7	6.2	
					22.5	22.5	5.73	5.97	76.5	80.3	3.92	5.66	4.8	5.7			
					22.5	19.1	5.74	5.35	76.8	72.2	3.95	5.55	5.0	6.5			

# Mid-Flood Tide

## Monitoring Station : TM-FC1

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)		Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Depth-average
22/05/14	1415-1430	29/Cloudy	Surface	1.0	26.6	18.3	18.4	5.79	5.80	78.6	78.7	3.02	3.05	4.0	4.1	4.4	
						18.4	5.81	78.8	3.08	4.2							
			Middle	10.6	26.7	18.6	18.6	5.14	5.15	69.9	70.1	3.26	3.23	4.2	4.3		
						18.6	5.16	70.2	3.20	4.4							
			Bottom	20.2	26.8	18.7	18.7	5.09	5.09	69.4	69.3	3.54	3.53	4.6	4.7		
						18.7	5.08	69.2	3.51	4.8							
24/05/14	1539-1600	27/Fine	Surface	1.0	26.8	12.2	12.3	5.42	5.43	71.9	72.0	3.50	3.51	4.4	4.5	4.6	
						12.4	5.43	72.0	3.52	4.6							
			Middle	10.9	26.7	12.6	12.6	5.19	5.20	68.9	69.1	3.61	3.62	4.4	4.5		
						12.5	5.21	69.2	3.63	4.6							
			Bottom	20.8	26.7	12.8	12.8	5.09	5.10	67.6	67.7	3.71	3.70	4.8	4.8		
						12.7	5.10	67.8	3.69	4.8							
27/05/14	1841-1900	30/Fine	Surface	1.0	27.2	20.0	20.0	5.91	5.90	90.7	90.6	4.96	4.95	6.0	5.9	6.4	
						19.9	5.89	90.4	4.93	5.8							
			Middle	11.4	26.8	22.5	22.5	5.46	5.45	83.9	83.7	5.60	5.58	6.6	6.7		
						22.4	5.43	83.5	5.55	6.8							
			Bottom	21.8	26.6	22.7	22.7	5.32	5.30	82.0	81.7	5.71	5.69	6.8	6.6		
						22.6	5.27	81.3	5.67	6.4							
29/05/14	1921-1930	33/Fine	Surface	1.0	27.1	19.9	20.0	5.93	5.94	83.2	83.3	4.72	4.71	5.6	5.7	6.2	
						20.0	5.95	83.4	4.70	5.8							
			Middle	11.4	26.6	22.2	22.3	5.46	5.47	76.9	77.0	5.33	5.32	6.2	6.3		
						22.3	5.48	77.1	5.30	6.4							
			Bottom	21.8	26.4	22.4	22.5	5.29	5.30	74.7	74.8	5.44	5.45	6.4	6.5		
						22.5	5.31	74.9	5.46	6.6							
31/05/14	0812-0830	31/Fine	Surface	1.0	27.2	19.8	19.9	6.02	6.03	84.4	84.5	4.72	4.71	5.6	5.7	6.1	
						19.9	6.04	84.6	4.70	5.8							
			Middle	11.4	26.6	22.2	22.3	5.58	5.57	78.7	78.6	5.28	5.29	6.2	6.3		
						22.3	5.56	78.5	5.30	6.4							
			Bottom	21.7	26.5	22.4	22.4	5.24	5.25	74.0	74.1	5.31	5.30	6.4	6.3		
						22.4	5.26	74.2	5.29	6.2							



# Mid-Flood Tide



東業 德 動 測 試 顧 問 有 限 公 司  
ETS-TESTCONSULT LIMITED

## Monitoring Station : TM-FM1

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)		Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average
03/05/14	0847-0904	24/Fine	Surface	23.8	26.6	26.6	6.05	6.06		82.6	82.8	3.17	3.19	4.2	4.3		
					26.5		6.07		82.9	3.21	4.4						
					26.7	26.8	5.98	5.97	81.8	3.28	4.4	3.26	4.3	4.4			
08/05/14	1416-1431	22/Cloudy	Surface	23.6	26.9	26.7	5.96	5.85		81.5	80.0	3.26	3.33	4.2	4.5		
					26.6		5.83	5.85	79.8	3.31	4.4						
					26.8	27.2	5.86	5.35	80.2	3.34	4.6	3.62	4.7	4.6			
10/05/14	1616-1632	22/Cloudy	Surface	21.6	27.1	27.2	5.32	5.35		74.1	74.1	3.61	3.62	4.8	4.7		
					27.2		5.38	5.26	74.5	3.63	4.8						
					27.2	27.3	5.16	5.17	71.6	3.89	4.8	3.90	4.9	5.0			
13/05/14	1820-1838	25/Cloudy	Surface	23.8	27.3	27.3	5.18	5.28		71.9	71.8	3.91	3.89	5.0	5.0		
					27.2		5.33	5.35	72.6	3.83	4.8						
					27.3	27.2	5.27	5.28	72.2	3.90	5.0	4.25	5.3	5.4			
15/05/14	1836-1851	27/Cloudy	Surface	25.5	27.4	27.4	5.01	5.05		69.7	70.3	4.21	3.89	4.6	4.7		
					27.4		5.09	5.82	74.2	3.88	4.6						
					26.9	27.0	5.43	5.42	74.2	3.88	4.6	3.89	4.7	4.8			
17/05/14	0810-0825	25/Rainy	Surface	25.7	27.0	27.3	5.41	5.35		73.1	72.9	3.90	3.81	4.4	4.5		
					27.2		5.36	5.53	73.1	3.79	4.6						
					27.3	27.3	5.33	5.53	72.6	3.83	4.8	3.86	4.7	4.8			
20/05/14	1016-1033	25/Cloudy	Surface	24.8	27.1	27.2	5.27	5.28		72.2	72.3	3.90	3.89	5.0	4.8		
					27.3		5.28	5.82	72.3	3.88	4.6						
					27.3	21.3	5.81	5.82	76.8	3.64	4.4	3.66	4.5	4.6			
13/05/14	1820-1838	25/Cloudy	Surface	23.8	21.2	21.3	5.82	5.82		76.9	76.9	3.67	3.66	4.4	4.5		
					22.2		5.43	5.42	72.4	3.89	4.8						
					22.0	22.1	5.41	5.42	72.2	3.92	5.2	3.84	5.0	5.1			
15/05/14	1836-1851	27/Cloudy	Surface	25.5	22.4	22.4	5.21	5.23		69.6	69.9	3.97	3.97	5.0	5.1		
					22.3		5.25	5.95	70.1	3.97	5.2						
					17.6	17.6	5.94	5.95	80.3	3.70	4.6	3.72	4.7	4.8			
17/05/14	0810-0825	25/Rainy	Surface	25.3	17.8	17.8	5.54	5.53		80.4	80.4	3.74	3.72	4.8	4.7		
					17.8		5.52	5.74	75.0	3.46	4.4						
					17.8	17.8	5.52	5.53	74.8	3.49	4.4	3.49	4.5	4.6			
17/05/14	0810-0825	25/Rainy	Surface	25.0	18.3	18.3	5.48	5.45		74.5	74.1	3.29	3.28	4.2	4.3		
					18.3		5.42	5.93	79.6	4.83	4.4						
					15.4	15.4	5.92	5.77	79.9	4.80	5.8	4.82	5.9	6.0			
17/05/14	0810-0825	25/Rainy	Surface	25.3	15.4	15.4	5.94	5.62		75.8	75.6	6.07	6.05	7.2	7.1		
					18.7		5.63	5.50	75.4	6.02	7.0						
					18.7	18.7	5.60	5.50	74.5	5.98	6.8	5.96	6.9	7.0			
20/05/14	1016-1033	25/Cloudy	Surface	24.9	19.3	19.4	5.52	5.50		74.5	74.3	5.94	5.96	6.8	6.9		
					19.3		5.48	5.71	74.0	5.94	7.0						
					15.2	15.3	5.86	5.87	78.8	4.74	5.6	4.73	5.7	5.8			
20/05/14	1016-1033	25/Cloudy	Surface	25.6	15.3	15.3	5.88	5.87		79.1	79.0	4.71	4.73	5.8	5.7		
					18.5		5.57	5.56	75.0	5.98	7.0						
					18.6	18.6	5.54	5.44	74.6	5.93	6.8	5.96	6.9	7.0			
20/05/14	1016-1033	25/Cloudy	Surface	25.2	19.3	19.3	5.46	5.44		73.8	73.5	5.86	5.86	6.8	6.9		
					19.3		5.42	5.44	73.2	5.85	7.0						
					19.3	19.3	5.46	5.44	73.8	5.86	6.8	5.86	6.9	7.0			

# Mid-Flood Tide

## Monitoring Station : TM-FM1

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
22/05/14	1346-1401	29/Cloudy	Surface	1.0	26.7	18.3	18.3	5.94	5.93		80.6	80.4	3.10	3.12		4.2	4.1	
						18.3	18.3	5.91		80.2		3.14		4.0				
						18.6	18.7	5.30	5.34	72.1	72.7	3.36	3.38	4.4	4.3	4.4		
			Middle	8.9	26.8	18.7	18.7	5.38		73.2		3.39		3.38		4.2		
						18.7	18.8	5.20	5.21	70.7	70.9	3.62	3.63	4.8	4.7			
						18.8	18.8	5.22		71.0		3.64		4.6				
24/05/14	1517-1833	27/Fine	Surface	1.0	26.7	12.3	12.4	5.35	5.36		70.9	71.0	3.43	3.44		4.2	4.3	
						12.4	12.4	5.36		71.1		3.45		4.4				
						12.5	12.6	5.18	5.18	68.8	68.8	3.61	3.62	4.6	4.7	4.6		
			Middle	9.0	26.9	12.6	12.6	5.17		68.7		3.62		3.59		4.8		
						12.9	12.9	5.03	5.05	66.8	67.1	3.70	3.71	4.8	4.7			
						12.8	12.8	5.07		67.4		3.71		4.8				
27/05/14	1816-1833	30/Fine	Surface	1.0	27.1	19.9	19.9	5.81	5.82		89.1	89.3	4.86	4.85		5.8	5.7	
						19.8	19.8	5.83		89.4		4.83		5.6				
						22.3	22.4	5.52	5.51	84.8	84.6	6.10	6.08	7.0	7.0	6.5		
			Middle	8.6	26.7	22.4	22.4	5.49		84.4		6.05		5.64		7.0		
						22.6	22.6	5.41	5.39	83.3	83.1	6.01	5.99	7.0	6.9			
						22.6	22.6	5.37		82.8		5.97		6.8				
29/05/14	1848-1906	33/Fine	Surface	1.0	27.0	19.9	19.9	5.80	5.81		81.4	81.5	4.80	4.81		5.8	5.7	
						19.9	19.9	5.82		81.6		4.82		5.6				
						22.3	22.4	5.52	5.53	77.8	77.9	5.77	5.78	6.8	6.7	6.4		
			Middle	8.6	26.7	22.4	22.4	5.54		78.0		5.79		5.50		6.6		
						22.4	22.5	5.36	5.37	75.7	75.8	5.92	5.91	7.0	6.9			
						22.5	22.5	5.38		75.9		5.90		6.8				
31/05/14	0748-0806	31/Fine	Surface	1.0	27.1	19.8	19.8	5.84	5.85		81.9	82.0	4.66	4.67		5.6	5.7	
						19.8	19.8	5.86		82.1		4.67		5.8				
						22.1	22.2	5.53	5.52	78.0	77.9	5.68	5.69	6.6	6.7	6.4		
			Middle	8.6	26.8	22.2	22.2	5.51		77.8		5.70		5.41		6.6		
						22.2	22.2	5.51	5.35	75.5	75.6	5.87	5.88	6.8	6.7			
						22.3	22.4	5.34		75.5		5.87		6.8				
Bottom	16.1	26.6	22.4	22.4	5.36	5.35	75.6	75.6	5.89	5.88	6.7							
			22.4	22.4	5.36		75.6		5.89		6.6							

# Mid-Flood Tide



東業 德勤 測 試 顧 問 有 限 公 司  
ETS-TESTCONSULT LIMITED

## Monitoring Station : TM-FM2

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
03/05/14	0823-0840	24/Fine	Surface	23.9	26.9	6.13	6.14	83.7	83.9	3.78	3.80	4.6	4.7	4.8				
				23.9	26.7	6.15	6.08	84.0	83.2	3.81	3.85	4.8	4.9					
			Middle	23.8	26.8	6.07	6.04	83.0	82.7	3.84	3.90	5.0	4.9		4.8			
				23.8	26.8	6.09	6.04	83.3	82.8	3.86	3.90	4.8	4.9					
			Bottom	23.6	26.7	6.03	5.53	82.6	76.6	3.89	3.41	4.4	4.5		4.8			
				23.6	27.2	5.56	5.38	82.8	76.2	3.90	3.41	4.4	4.5					
08/05/14	1353-1408	22/Cloudy	Surface	23.4	27.3	5.24	5.23	72.7	72.5	3.63	3.65	4.8	4.8	4.8				
				23.2	27.4	5.21	5.12	72.3	71.2	3.67	4.14	4.8	5.1					
			Middle	21.7	27.5	5.10	5.12	70.9	71.5	4.18	4.10	5.2	5.0		5.0			
				21.7	27.6	5.14	5.86	71.5	80.2	4.10	3.97	5.0	5.0					
			Bottom	21.6	27.1	5.68	5.71	77.8	77.6	4.01	4.05	4.8	4.9		5.0			
				21.6	27.2	5.65	5.67	78.0	77.8	4.07	4.02	5.2	5.1					
10/05/14	1553-1609	22/Cloudy	Surface	23.7	20.9	5.71	5.72	75.8	75.7	3.53	3.53	4.4	4.4	4.8				
				23.7	21.9	5.54	5.55	75.5	74.1	3.52	3.63	4.4	4.8					
			Middle	23.5	22.2	5.56	5.33	74.2	71.1	3.61	3.91	4.8	5.1		5.0			
				23.5	22.5	5.31	5.33	70.9	71.3	3.93	3.91	5.2	5.0					
			Bottom	25.6	17.5	5.90	5.91	79.8	79.9	3.48	3.44	4.6	4.7		4.8			
				25.6	17.5	5.91	5.47	79.9	74.4	3.40	3.05	4.8	4.2					
13/05/14	1754-1814	25/Cloudy	Surface	25.3	17.7	5.46	5.47	74.8	74.8	3.02	3.08	4.0	4.2	4.8				
				25.3	18.2	5.29	5.34	71.9	72.1	3.85	3.84	4.4	5.2					
			Middle	25.8	15.4	5.98	5.97	80.4	80.6	4.92	4.94	5.8	5.9		6.6			
				25.8	15.4	5.95	5.58	80.8	75.1	4.95	5.77	6.0	6.7					
			Bottom	24.8	18.5	5.59	5.44	75.3	73.5	5.79	5.93	6.6	7.2		7.2			
				24.8	19.3	5.56	5.44	74.9	73.2	5.75	5.91	6.8	7.2					
15/05/14	1818-1833	27/Cloudy	Surface	25.0	18.3	5.39	5.34	72.2	72.1	3.83	3.84	5.2	5.2	6.5				
				25.0	19.3	5.42	5.38	73.2	73.5	5.91	5.93	7.2	7.2					
			Middle	25.7	15.2	5.92	5.91	79.6	79.8	4.83	4.85	5.8	5.7		6.5			
				25.7	15.3	5.89	5.52	80.0	74.3	4.86	5.68	5.6	6.8					
			Bottom	24.7	18.4	5.53	5.38	74.5	72.8	5.70	5.84	6.8	6.9		7.0			
				24.7	18.3	5.50	5.38	74.1	72.5	5.66	5.82	6.8	7.0					
17/05/14	0750-0805	25/Rainy	Surface	24.7	19.1	5.36	5.38	73.0	72.8	5.86	5.84	6.8	6.9	6.5				
				24.7	19.2	5.40	5.38	73.0	72.5	5.86	5.84	7.0	6.9					
			Middle	24.8	19.3	5.42	5.44	73.2	73.5	5.91	5.93	7.2	7.2		6.6			
				24.8	19.3	5.42	5.44	73.2	73.5	5.91	5.93	7.2	7.2					
			Bottom	25.1	18.3	5.50	5.38	74.1	72.8	5.66	5.84	6.8	6.9		7.0			
				25.1	18.4	5.53	5.38	74.5	72.8	5.66	5.84	6.8	6.9					
20/05/14	0953-1010	25/Cloudy	Surface	25.1	18.4	5.53	5.38	74.1	72.8	5.66	5.84	6.8	6.9	6.5				
				25.1	18.3	5.50	5.38	74.1	72.5	5.66	5.84	6.8	6.9					
			Middle	24.7	19.2	5.40	5.38	73.0	72.8	5.86	5.84	6.8	6.9		7.0			
				24.7	19.1	5.36	5.38	73.0	72.5	5.86	5.84	7.0	6.9					
			Bottom	25.1	18.4	5.53	5.38	74.5	72.8	5.66	5.84	6.8	6.9		7.0			
				25.1	18.3	5.50	5.38	74.1	72.5	5.66	5.84	6.8	6.9					

# Mid-Flood Tide

## Monitoring Station : TM-FM2

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Value	Depth-average	Value	Average	Depth-average
22/05/14	1323-1338	29/Cloudy	Surface	26.7	18.3	18.4	5.82	5.84	79.0	79.2	3.06	3.07	4.0	4.0	4.6			
					18.4		5.85		79.4		3.08		4.0					
					18.7	18.7	5.61	5.65	76.3	76.5	3.60	3.61	4.8	4.8				
24/05/14	1456-1511	27/Fine	Middle	26.8	18.7	18.7	5.68	5.65	76.6	76.5	3.61	3.61	4.8	4.8	4.5			
					18.8	18.8	5.44	5.44	74.1	74.0	3.83	3.84	5.2	5.0				
					18.7	18.8	5.43	5.44	73.9	74.0	3.85	3.84	4.8	5.0				
27/05/14	1753-1810	30/Fine	Surface	27.1	12.2	12.3	5.55	5.55	73.6	73.6	3.31	3.32	4.0	4.1	6.6			
					12.4	12.4	5.54	5.47	73.5	84.0	3.33	5.80	4.2	6.8				
					12.4	12.5	5.21	5.22	69.2	69.4	3.48	3.48	4.6	6.8				
29/05/14	1824-1842	33/Fine	Middle	26.7	12.6	12.5	5.23	5.48	69.5	77.2	3.47	5.73	4.8	6.8	6.4			
					12.8	12.8	5.09	5.49	67.6	77.3	3.69	5.74	4.8	6.8				
					12.7	12.8	5.12	5.33	68.0	82.2	3.67	5.96	4.6	7.2				
31/05/14	0724-0742	31/Fine	Bottom	26.7	20.0	20.0	5.87	5.72	89.6	81.2	4.95	4.94	5.8	5.7	6.5			
					19.9	20.0	5.84	5.79	90.0	81.3	4.98	4.95	5.8	5.6				
					22.4	22.3	5.45	5.48	83.8	77.1	5.78	5.72	6.8	6.8				
27/05/14	1753-1810	30/Fine	Surface	27.1	22.5	22.5	5.35	5.33	82.4	82.2	5.98	5.96	7.2	7.2	6.6			
					22.4	22.4	5.31	5.28	81.9	81.2	5.94	4.93	7.2	5.7				
					19.9	20.0	5.78	5.79	81.1	81.2	4.93	4.94	5.8	5.7				
29/05/14	1824-1842	33/Fine	Middle	26.7	22.2	22.3	5.47	5.48	77.1	77.2	4.95	5.73	6.8	6.8	6.4			
					22.2	22.3	5.47	5.48	77.1	77.2	4.95	5.73	6.8	6.8				
					22.3	22.3	5.49	5.48	77.3	77.3	5.74	5.74	6.8	6.8				
31/05/14	0724-0742	31/Fine	Bottom	26.7	22.4	22.4	5.29	5.28	74.7	74.6	5.88	5.87	6.8	6.7	6.5			
					22.4	22.4	5.27	5.28	74.5	74.6	5.86	5.87	6.6	6.7				
					19.9	20.0	5.73	5.72	80.3	80.2	4.89	4.90	5.8	5.9				
27/05/14	1753-1810	30/Fine	Surface	27.0	20.0	20.0	5.71	5.72	80.1	80.2	4.91	4.90	6.0	5.9	6.5			
					20.0	20.0	5.71	5.72	80.1	80.2	4.91	4.90	6.0	5.9				
					22.2	22.3	5.42	5.41	76.5	76.4	5.74	5.75	6.8	6.8				
31/05/14	0724-0742	31/Fine	Middle	26.9	22.2	22.3	5.42	5.41	76.5	76.4	5.74	5.75	6.8	6.8	6.5			
					22.2	22.3	5.42	5.41	76.5	76.4	5.74	5.75	6.8	6.8				
					22.3	22.3	5.40	5.41	76.3	76.4	5.76	5.75	6.8	6.8				
27/05/14	1753-1810	30/Fine	Bottom	27.1	22.4	22.4	5.22	5.23	73.7	73.8	5.80	5.81	7.0	6.9	6.6			
					22.4	22.4	5.22	5.23	73.7	73.8	5.80	5.81	7.0	6.9				
					22.3	22.3	5.24	5.23	73.9	73.8	5.82	5.81	7.0	6.9				

# Mid-Flood Tide



東業德勤測試顧問有限公司  
ETS-TESTCONSULT LIMITED

## Monitoring Station : TM-FC2

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)		Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average
03/05/14	0800-0817	24/Fine	Surface	23.9	26.7	26.8	6.18	6.19	6.17	84.4	84.6	3.65	3.66	4.4	4.5	4.7	
			Middle	23.9	26.8	6.13	6.14	83.9	84.0	3.72	3.73	4.8	4.7				
			Bottom	23.8	26.9	6.15	6.10	84.1	83.5	3.74	3.81	4.6	5.0	5.0			
08/05/14	1330-1345	22/Cloudy	Surface	23.6	27.1	27.1	5.66	5.68	5.52	78.4	78.6	3.32	3.35	4.4	4.5	4.7	
			Middle	23.3	27.2	5.34	5.36	74.1	74.3	3.45	3.43	4.6	4.5				
			Bottom	23.2	27.3	5.38	5.03	74.5	70.0	3.41	4.01	4.4	5.0	5.1			
10/05/14	1530-1546	22/Cloudy	Surface	21.6	26.8	26.9	5.65	5.66	5.59	77.2	77.4	3.91	3.92	4.8	4.9	5.0	
			Middle	21.6	27.1	5.54	5.53	75.5	75.3	3.95	3.95	5.2	5.1				
			Bottom	21.6	27.0	5.51	5.41	75.1	74.2	3.94	3.98	5.0	5.2	5.1			
13/05/14	1730-1748	25/Cloudy	Surface	23.8	21.1	21.2	5.02	5.02	5.29	74.3	74.3	3.34	3.36	4.2	4.3	4.6	
			Middle	23.6	21.9	22.0	5.55	5.56	74.1	74.2	3.65	3.65	4.4	4.7			
			Bottom	23.4	22.1	22.2	5.39	5.36	74.2	71.5	3.64	3.89	4.8	4.7			
15/05/14	1800-1815	27/Cloudy	Surface	25.6	17.6	17.3	5.89	5.85	5.75	79.6	79.1	3.66	3.65	4.8	4.7	4.5	
			Middle	25.3	17.9	17.9	5.64	5.65	78.5	76.4	3.64	3.13	4.6	4.1			
			Bottom	25.0	18.3	18.4	5.30	5.32	76.3	72.3	3.12	3.63	4.0	4.2	4.7		
17/05/14	0730-0745	25/Rainy	Surface	25.8	15.3	15.3	5.95	5.93	5.79	80.0	79.8	5.03	5.05	6.0	6.0	6.3	
			Middle	25.2	18.4	18.4	5.67	5.65	76.4	76.2	5.43	5.42	6.0	6.5			
			Bottom	24.9	19.3	19.4	5.53	5.52	75.9	74.5	5.40	5.50	6.6	6.5			
20/05/14	0930-0947	25/Cloudy	Surface	25.7	15.2	15.2	5.89	5.87	5.73	74.3	79.0	4.94	4.96	5.8	6.0	6.2	
			Middle	25.1	18.2	18.3	5.61	5.59	78.7	75.4	5.34	5.33	6.2	6.3			
			Bottom	24.8	19.3	19.3	5.47	5.46	75.1	73.8	5.31	5.41	6.4	6.3			

# Mid-Flood Tide

## Monitoring Station : TM-FC2

Date	Sampling Duration	Ambient Temp (°C)/ Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	
22/05/14	1300-1315	29/Cloudy	Surface	1.0	26.7	18.4	18.4	5.77	5.74	79.3	78.4	3.47	3.48	4.4	4.3	4.5		
						18.4	5.71	77.5	3.49	4.2								
			Middle	8.3	26.8	18.6	18.6	5.50	5.52	74.8	75.1	3.59	3.57	4.6	4.7			
	18.6					5.54	75.3	3.54	4.8									
	Bottom					15.6	26.8	18.7	18.8	5.10	5.12	69.5	69.8	3.45	3.43		4.4	4.5
			18.8	5.14	70.0			3.41	4.6									
24/05/14	1435-1450	27/Fine	Surface	1.0	26.8	12.4	12.4	5.61	5.62	74.4	74.6	3.35	3.36	4.2	4.3	4.5		
						12.3	5.63	74.7	3.37	4.4								
			Middle	8.5	26.8	12.5	12.6	5.31	5.30	70.5	70.4	3.42	3.44	4.6	4.5			
						12.7	5.29	70.3	3.46	4.4								
						Bottom	16.0	26.7	12.9	12.9	5.04	5.04	70.0	68.4	3.49		3.50	4.6
			12.8	5.03	66.8				3.51	4.8								
27/05/14	1730-1747	30/Fine	Surface	1.0	27.0	19.9	20.0	5.84	5.82	89.5	89.3	5.06	5.08	6.0	6.0	6.4		
						20.0	5.80	89.0	5.09	6.0								
			Middle	8.4	26.6	22.3	22.4	5.56	5.54	85.5	85.3	5.46	5.45	6.4	6.5			
						22.4	5.52	85.0	5.43	6.6								
						Bottom	15.8	26.5	22.6	22.6	5.42	5.41	83.5	83.3	5.54		5.53	6.6
			22.5	5.39	83.1				5.51	6.8								
29/05/14	1800-1818	33/Fine	Surface	1.0	27.2	19.8	19.9	5.89	5.88	82.6	82.5	4.92	4.93	6.0	5.9	6.4		
						19.9	5.87	82.4	4.94	5.8								
			Middle	8.4	26.6	22.1	22.2	5.55	5.56	78.2	78.3	5.46	5.47	6.4	6.5			
						22.2	5.57	78.4	5.48	6.6								
						Bottom	15.7	26.5	22.3	22.4	5.40	5.39	76.3	76.2	5.57		5.58	6.6
			22.4	5.38	76.1				5.59	6.8								
31/05/14	0700-0718	31/Fine	Surface	1.0	27.1	20.0	20.1	5.95	5.96	83.4	83.5	4.82	4.81	5.6	5.7	6.3		
						20.1	5.97	83.6	4.80	5.8								
			Middle	8.4	26.8	22.2	22.2	5.68	5.67	80.2	80.3	5.43	5.42	6.4	6.5			
						22.1	5.66	80.4	5.41	6.6								
						Bottom	15.8	26.6	22.3	22.4	5.42	5.43	76.6	76.7	5.55		5.56	6.4
			22.4	5.44	76.8				5.57	6.8								

**Mid-Ebb Tide**

**Monitoring Station : TM-FC1**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
03/05/14	1541-1600	24/Fine	Surface	23.9	26.3	26.4	5.90	5.90	5.86	80.6	80.6	3.94	3.96	4.8	4.9	5.1		
			Middle	23.8	26.7	26.8	5.81	5.82	79.5	79.6	4.06	4.07	5.0	5.1				
			Bottom	23.9	26.8	26.8	5.82	5.77	79.6	79.0	4.07	4.14	5.2	5.3				
08/05/14	0845-0900	22/Cloudy	Surface	23.7	27.2	27.2	5.76	5.73	5.53	79.8	79.4	3.59	3.57	4.6	4.5	4.8		
			Middle	23.4	27.4	27.4	5.34	5.33	74.1	73.9	3.87	3.84	4.8	4.9				
			Bottom	23.2	27.6	27.6	5.31	5.22	73.7	72.7	3.81	4.16	5.0	5.1				
10/05/14	1108-1130	22/Cloudy	Surface	21.6	27.1	27.1	5.24	5.50	5.41	72.4	75.1	4.14	4.10	5.0	5.1	5.2		
			Middle	21.7	27.2	27.2	5.49	5.33	72.8	72.7	4.18	4.17	5.4	5.3				
			Bottom	21.7	26.8	26.9	5.32	5.12	72.5	70.1	4.18	4.18	5.2	5.3				
13/05/14	1144-1200	27/Cloudy	Surface	24.1	21.2	21.3	6.02	6.01	5.94	79.7	79.5	3.63	3.64	4.6	4.7	4.8		
			Middle	23.9	21.3	21.3	5.99	5.88	79.2	78.5	3.64	3.74	4.8	4.6				
			Bottom	23.8	22.2	22.2	5.86	5.88	78.3	78.7	3.75	3.72	4.6	4.6				
15/05/14	1415-1430	28/Cloudy	Surface	25.5	22.6	22.7	5.67	5.65	5.65	75.8	75.5	4.13	4.11	5.2	5.1	4.7		
			Middle	25.3	22.7	22.7	5.63	5.87	79.5	79.4	4.09	3.73	5.0	4.7				
			Bottom	25.1	17.4	17.5	5.88	5.45	79.2	73.9	3.70	3.53	4.6	4.3				
17/05/14	1530-1545	25/Rainy	Surface	25.9	15.3	15.3	5.43	5.12	5.12	74.2	69.7	3.51	4.02	4.2	5.1	6.6		
			Middle	25.2	18.8	18.8	5.67	5.65	76.4	76.2	3.54	5.96	4.4	6.7				
			Bottom	25.1	19.0	19.0	5.63	5.56	75.9	75.0	3.51	6.03	4.4	7.1				
20/05/14	1741-1800	25/Cloudy	Surface	25.8	15.3	15.4	5.14	5.88	5.64	70.0	79.5	4.00	4.89	5.8	5.9	6.3		
			Middle	25.2	18.6	18.6	5.54	5.41	78.9	73.2	4.04	5.52	6.0	6.4				
			Bottom	25.1	19.1	19.2	5.28	5.26	72.8	71.0	4.87	5.63	6.4	6.7				

**Mid-Ebb Tide**



**Monitoring Station : TM-FC1**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	
22/05/14	0845-0900	29/Cloudy	Surface	1.0	26.7	18.4	18.4	5.72	5.75	77.6	78.1	2.78	2.79	3.6	3.7	4.4		
						18.4	5.78	78.5	2.80	3.8								
			Middle	10.4	26.7	18.6	18.7	5.28	5.29	71.8	72.0	3.40	3.42	4.4	4.5			
						18.7	5.30	72.2	3.43	4.6								
			Bottom	19.8	26.9	18.8	18.8	5.11	5.12	69.5	69.7	3.87	3.84	5.0	5.0			
						18.8	5.13	69.9	3.81	5.0								
24/05/14	1008-1028	27/Fine	Surface	1.0	26.8	12.3	12.4	5.35	5.36	70.9	71.0	3.58	3.49	4.6	4.4	4.7		
						12.4	5.36	71.1	3.40	4.2								
			Middle	10.3	26.7	12.6	12.7	5.11	5.12	67.9	68.0	3.68	3.69	4.6	4.7			
						12.7	5.13	68.1	3.70	4.8								
			Bottom	20.6	26.8	12.9	12.9	5.02	5.03	66.7	66.8	3.80	3.80	5.0	4.9			
						12.8	5.03	66.8	3.79	4.8								
27/05/14	1211-1230	29/Fine	Surface	1.0	27.1	19.9	19.9	5.82	5.81	89.2	89.1	5.02	5.01	6.0	6.0	6.4		
						19.8	5.80	89.0	4.99	6.0								
			Middle	11.3	26.7	22.3	22.4	5.37	5.36	82.5	82.3	5.66	5.64	6.6	6.5			
						22.4	5.34	82.1	5.61	6.4								
			Bottom	21.6	26.6	22.5	22.6	5.23	5.21	80.5	80.2	5.77	5.75	6.8	6.7			
						22.6	5.18	79.8	5.73	6.6								
29/05/14	1312-1330	33/Fine	Surface	1.0	27.1	19.9	20.0	5.82	5.81	81.7	81.6	4.83	4.82	5.8	5.7	6.2		
						20.0	5.80	81.5	4.81	5.6								
			Middle	11.3	26.7	22.3	22.3	5.39	5.40	75.9	76.0	5.37	5.38	6.4	6.3			
						22.2	5.41	76.1	5.39	6.2								
			Bottom	21.5	26.5	22.4	22.5	5.22	5.21	73.7	73.6	5.49	5.50	6.4	6.5			
						22.5	5.20	73.5	5.51	6.6								
31/05/14	1442-1500	31/Fine	Surface	1.0	27.1	19.9	20.0	5.93	5.92	83.1	83.0	4.88	4.89	5.8	5.9	6.3		
						20.0	5.91	82.9	4.90	6.0								
			Middle	11.2	26.7	22.2	22.3	5.46	5.47	77.0	77.1	5.32	5.33	6.4	6.3			
						22.3	5.48	77.2	5.34	6.2								
			Bottom	21.4	26.6	22.4	22.5	5.19	5.18	73.3	73.2	5.43	5.44	6.6	6.6			
						22.5	5.17	73.1	5.45	6.5								



**Monitoring Station :** TM-FM1

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
03/05/14	1517-1534	24/Fine	Surface	23.9	26.5	26.5	5.93	5.94	5.92	81.0	81.1	81.1	3.24	3.26	3.26	4.2	4.1	
			Middle	23.8	26.8	26.8	5.90	5.90	5.92	80.7	80.7	80.7	3.31	3.32	3.33	4.4	4.5	4.3
			Bottom	23.9	26.9	26.9	5.89	5.78	5.78	80.6	79.2	79.2	3.33	3.41	3.39	4.4	4.3	
08/05/14	0827-0842	22/Cloudy	Surface	23.7	27.3	27.3	5.66	5.65	5.44	78.4	78.3	78.3	3.42	3.46	3.43	4.6	4.7	
			Middle	23.4	27.5	27.5	5.21	5.22	5.44	72.3	72.5	72.5	3.74	3.75	3.76	4.8	4.7	4.8
			Bottom	23.3	27.6	27.6	5.23	5.09	5.09	72.6	70.8	70.8	3.74	3.87	3.88	4.6	4.9	
10/05/14	1046-1102	22/Cloudy	Surface	21.6	27.1	27.1	5.35	5.34	5.31	70.7	73.0	73.0	3.86	3.97	3.96	5.0	5.0	
			Middle	21.7	27.1	27.1	5.29	5.27	5.31	72.1	71.9	71.9	3.85	3.88	3.85	4.8	4.9	4.9
			Bottom	21.8	27.0	27.0	5.25	5.21	5.21	71.6	71.3	71.3	3.90	3.98	3.99	5.0	4.9	
13/05/14	1121-1139	27/Cloudy	Surface	23.9	21.1	21.1	5.76	5.74	5.54	76.2	76.0	76.0	3.52	3.54	3.52	4.4	4.6	
			Middle	23.8	22.3	22.3	5.72	5.35	5.35	75.7	71.4	71.4	3.55	3.96	3.94	4.8	5.2	5.0
			Bottom	23.7	22.2	22.2	5.33	5.36	5.36	71.2	68.7	68.7	3.98	4.01	4.02	5.2	5.1	
15/05/14	1336-1351	28/Cloudy	Surface	25.4	17.5	17.5	5.80	5.80	5.68	78.4	78.4	78.4	3.66	3.68	3.66	4.8	4.8	
			Middle	25.3	17.7	17.7	5.79	5.57	5.57	78.3	75.5	75.5	3.69	3.98	3.99	4.8	5.1	5.0
			Bottom	25.2	17.7	17.7	5.56	5.25	5.25	75.4	71.4	71.4	3.96	4.14	4.18	5.2	5.2	
17/05/14	1510-1525	25/Rainy	Surface	25.9	15.4	15.4	5.22	5.86	5.80	70.9	78.8	78.8	4.18	5.05	5.03	6.0	6.2	
			Middle	25.3	18.9	18.9	5.76	5.75	5.75	77.7	77.5	77.5	5.88	5.86	5.88	6.4	6.9	6.6
			Bottom	25.1	19.1	19.1	5.43	5.41	5.41	73.4	73.1	73.1	5.79	5.77	5.74	6.6	6.7	
20/05/14	1716-1733	25/Cloudy	Surface	25.7	15.3	15.3	5.77	5.78	5.61	72.8	77.8	77.8	4.80	4.79	4.80	5.8	5.7	
			Middle	25.3	18.7	18.7	5.48	5.45	5.45	77.9	73.4	73.4	4.77	6.02	6.04	7.2	7.2	6.6
			Bottom	24.9	19.4	19.4	5.37	5.35	5.35	72.7	72.4	72.4	5.92	5.92	5.91	6.8	7.0	

**Monitoring Station : TM-FM1**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)																						
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average																				
22/05/14	0816-0832	29/Cloudy	Surface	26.8	18.4	5.63	5.65	76.4	3.12	3.13	4.2	4.1	4.6	Middle	26.8	18.6	5.44	5.45	74.0	3.72	3.76	4.8	4.7	4.6	Bottom	26.8	18.8	5.13	5.12	69.9	3.93	3.95	5.0	4.9	4.8			
				26.8	18.7	5.11	5.12	69.6	3.96	3.95	4.8	4.9																										
			Surface	26.8	12.2	5.27	5.28	70.0	3.50	3.51	4.6	4.7		4.8	Middle	26.8	12.5	5.10	5.10	67.7	3.70	3.69	4.8	4.7	4.6	Bottom	26.7	12.8	4.95	4.98	65.8	3.78	3.79	4.8	4.7			
				26.7	12.4	5.09	5.10	67.6	3.68	3.69	4.6	4.7																										
			27/05/14	1146-1203	29/Fine	Surface	27.0	19.9	5.72	5.73	87.7	4.92		4.89	6.0	6.0	6.7	Middle	26.7	22.3	5.43	5.42	83.4	6.16	6.14	7.2	7.1	7.0	Bottom	26.5	22.5	5.32	5.30	82.0	6.07	6.05	7.0	7.1
							26.7	22.2	5.40	5.42	83.0	6.11		6.11	7.2	7.0																						
Surface	27.1	19.9				5.73	5.74	80.4	4.86	4.87	5.8	5.7	6.5	Middle	26.6	22.3		5.44	5.45	76.6	5.83	5.84	6.8	6.7	6.6	Bottom	26.4	22.4	5.27	5.28	74.4	6.02	6.03	7.0	7.1			
	26.4	22.4				5.29	5.28	74.6	6.04	6.04	7.2	7.1																										
31/05/14	1418-1436	31/Fine				Surface	27.2	20.1	5.77	5.76	80.9	4.76	4.77	5.6	5.8	6.5		Middle	26.8	22.1	5.42	5.41	76.5	5.73	5.72	6.8	6.7	6.6	Bottom	26.7	22.3	5.28	5.29	74.6	5.99	5.96	7.0	7.1
							26.7	22.4	5.30	5.29	74.8	5.92	5.92	7.2	7.1																							

**Monitoring Station : TM-FM2**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Value	Average
03/05/14	1453-1510	24/Fine	Surface	23.8	26.8	26.9	6.08	6.10		83.1	83.3	3.86	3.88	4.8	4.9			
					26.9		6.11		83.5		3.89		5.0					
					26.8	26.8	5.99	6.00	81.9	82.1	3.93	3.95	5.0	5.1	5.1	5.1		
08/05/14	0809-0824	22/Cloudy	Middle	23.9	26.7	26.8	6.01	6.00	82.2	82.1	3.97	3.95	5.2	5.1				
					26.8	26.9	5.95	5.96	81.5	81.6	3.98	3.99	5.4	5.3	5.3	5.3		
					26.9		5.97		81.7		3.99		5.2					
10/05/14	1023-1039	22/Cloudy	Surface	23.6	27.1	27.2	5.59	5.57	77.4	77.1	3.21	3.22	4.2	4.3				
					27.2		5.54		76.7		3.23		4.4					
					27.4	27.5	5.17	5.14	71.8	71.4	3.46	3.43	4.4	4.5	4.5	4.5		
13/05/14	1055-1115	27/Cloudy	Bottom	23.2	27.5	27.6	5.11	5.46	70.9	76.0	3.40	3.73	4.6	4.7				
					27.6		5.44		75.7		3.72		4.8					
					27.5	27.5	5.48	5.46	76.3	76.0	3.73	3.73	4.6	4.7	4.7	4.7		
15/05/14	1318-1333	28/Cloudy	Surface	21.7	27.1	27.2	5.56	5.57	75.9	76.1	4.07	4.09	4.8	4.9				
					27.2		5.58		76.2		4.10		5.0					
					27.2	27.2	5.60	5.66	76.7	77.2	4.12	4.13	5.2	5.1	5.1	5.1		
17/05/14	1450-1505	25/Rainy	Middle	25.3	27.3	27.3	5.69	5.59	77.6	76.6	4.14	4.10	4.8	4.5				
					27.2		5.58		76.4		4.11		4.8					
					21.0	21.1	5.62	5.65	74.3	74.8	3.39	3.41	4.4	4.5	4.5	4.5		
20/05/14	1653-1710	25/Cloudy	Bottom	24.8	22.1	22.2	5.41	5.43	72.2	72.4	3.43	3.58	4.6	4.7				
					22.2		5.44		72.6		3.57		4.6					
					22.4	22.5	5.24	5.24	70.1	70.1	3.87	3.86	4.8	4.7	4.7	4.7		
17/05/14	1318-1333	28/Cloudy	Surface	25.5	17.4	17.5	5.85	5.86	79.1	79.2	3.72	3.75	4.8	4.7				
					17.5		5.86		79.2		3.78		4.6					
					17.6	17.7	5.62	5.63	76.0	76.2	3.85	3.84	4.8	4.9	4.9	4.9		
17/05/14	1450-1505	25/Rainy	Middle	24.9	17.7	17.7	5.64	5.63	76.3	76.2	3.83	3.84	5.0	4.9				
					18.4	18.4	5.10	5.13	69.3	69.7	4.09	4.07	5.2	5.1	5.1	5.1		
					18.4		5.16		70.1		4.04		5.0					
17/05/14	1450-1505	25/Rainy	Bottom	25.1	15.3	15.3	5.95	5.97	80.0	80.2	5.09	5.12	6.0	6.1				
					15.3		5.98		80.4		5.14		6.2					
					18.9	18.9	5.69	5.67	76.8	76.5	5.43	5.42	6.4	6.5	6.5	6.5		
17/05/14	1450-1505	25/Rainy	Bottom	24.9	18.9	19.2	5.65	5.62	76.2	76.0	5.40	5.68	6.6	6.7				
					19.2		5.64		75.7		5.69		6.8					
					19.2		5.64		76.2		5.66		6.6					
20/05/14	1653-1710	25/Cloudy	Surface	25.8	15.3	15.4	5.83	5.82	78.5	78.7	4.89	4.91	5.8	5.7				
					15.4		5.80		78.8		4.92		5.6					
					18.4	18.5	5.44	5.43	73.3	73.1	5.76	5.74	6.8	6.7	6.7	6.7		
20/05/14	1653-1710	25/Cloudy	Middle	25.2	18.5	18.5	5.41	5.43	72.9	73.1	5.72	5.74	6.6	6.7				
					18.5		5.41		73.3		5.72		6.6					
					19.3	19.4	5.31	5.29	71.8	71.6	5.92	5.90	7.2	7.1	7.1	7.1		
20/05/14	1653-1710	25/Cloudy	Bottom	24.8	19.4	19.4	5.27	5.29	71.4	71.6	5.88	5.90	7.0	7.1				
					19.4		5.27		71.4		5.88		7.0					
					19.4		5.27		71.4		5.88		7.0					



**Monitoring Station : TM-FM2**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)				
					Value	Average	Value	Average	Depth-average	Value	Average	Value	Average	Depth-average	Value	Average	Depth-average			
22/05/14	0753-0808	29/Cloudy	Surface	1.0	26.8	18.4	18.5	5.79	5.80	5.65	78.6	78.8	3.37	3.34	4.4	4.3	4.6	4.6		
						18.5		5.81			78.9		3.30						4.2	
			Middle	9.1	26.8	18.7	18.7	5.50	5.50	74.8	74.8	3.66	3.63	4.8	4.7	4.6	4.7	4.6	4.6	
						18.7		5.49		74.7										3.60
			Bottom	17.2	26.8	18.8	18.8	5.36	5.35	72.9	72.8	3.74	3.73	4.8	4.7	4.6	4.7	4.6	4.6	4.6
						18.8		5.34		72.7										
24/05/14	0926-0941	27/Fine	Surface	1.0	26.8	12.4	12.4	5.48	5.49	5.32	72.7	72.8	3.38	3.39	4.2	4.3	4.6	4.6		
						12.3		5.50			72.9		3.40						4.4	
			Middle	9.2	26.7	12.5	12.5	5.14	5.15	68.3	68.4	3.56	3.57	4.6	4.7	4.6	4.7	4.6	4.6	
						12.5		5.16		68.5										3.57
			Bottom	17.4	26.7	12.9	12.8	5.01	5.03	66.6	66.8	3.77	3.76	4.8	4.7	4.6	4.7	4.6	4.6	4.6
						12.7		5.04		67.0										
27/05/14	1123-1140	29/Fine	Surface	1.0	27.0	19.8	19.8	5.78	5.77	5.57	88.6	88.4	5.01	5.03	6.0	6.0	6.6	6.6		
						19.7		5.75			88.2		5.04						6.0	
			Middle	8.6	26.6	22.3	22.4	5.39	5.38	82.8	82.6	5.88	5.86	6.8	6.7	6.6	6.7	6.6	6.6	
						22.4		5.36		82.4										5.84
			Bottom	16.2	26.5	22.6	22.6	5.26	5.24	81.0	80.7	6.04	6.02	7.0	7.1	7.2	7.1	7.0	7.0	7.0
						22.5		5.22		80.4										
29/05/14	1228-1245	33/Fine	Surface	1.0	27.0	20.0	20.0	5.67	5.68	5.53	79.6	79.7	5.02	5.03	6.0	6.1	6.6	6.6		
						20.0		5.69			79.8		5.04						6.2	
			Middle	8.6	26.7	22.2	22.3	5.38	5.37	75.8	75.7	5.80	5.81	6.6	6.7	6.6	6.7	6.6	6.6	
						22.3		5.36		75.6										5.82
			Bottom	16.2	26.5	22.4	22.5	5.13	5.14	72.4	72.5	5.99	5.98	7.0	6.9	7.0	6.9	6.8	6.8	6.8
						22.5		5.15		72.6										
31/05/14	1354-1412	31/Fine	Surface	1.0	27.1	20.1	20.2	5.65	5.66	5.52	79.2	79.3	4.92	4.93	5.8	5.9	6.6	6.6		
						20.2		5.67			79.4		4.94						6.0	
			Middle	8.6	26.7	22.3	22.4	5.39	5.38	76.1	76.0	5.83	5.84	6.8	6.7	6.6	6.7	6.6	6.6	
						22.4		5.37		75.9										5.85
			Bottom	16.1	26.6	22.4	22.5	5.16	5.17	72.9	73.0	5.92	5.93	7.2	7.1	7.2	7.1	7.0	7.0	7.0
						22.5		5.18		73.1										

**Monitoring Station : TM-FC2**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
03/05/14	1430-1447	24/Fine	Surface	23.9	26.8	26.8	6.11	6.12	6.09	83.5	83.6	83.6	3.74	3.75	3.75	4.8	4.7	
			Middle	23.8	26.7	26.8	6.05	6.06	6.06	82.8	82.9	82.9	3.80	3.81	3.82	4.6	4.8	4.8
			Bottom	23.9	26.9	26.8	6.00	6.02	6.02	82.1	82.4	82.4	3.89	3.90	3.91	4.8	5.0	5.2
08/05/14	0750-0806	22/Cloudy	Surface	23.7	27.2	27.2	5.40	5.41	5.38	74.8	75.0	75.0	3.02	3.06	3.09	4.0	3.9	
			Middle	23.5	27.4	27.4	5.36	5.35	5.35	74.4	74.3	74.3	3.63	3.64	3.64	4.6	4.7	4.5
			Bottom	23.2	27.5	27.5	5.12	5.13	5.13	71.3	71.4	71.4	3.99	3.95	3.91	5.0	4.9	4.8
10/05/14	1000-1016	22/Cloudy	Surface	21.6	27.0	27.0	5.59	5.59	5.51	76.7	76.6	76.6	3.99	4.01	4.01	4.8	4.9	
			Middle	21.7	27.2	27.2	5.45	5.44	5.44	74.3	74.2	74.2	4.01	4.02	4.03	5.0	4.9	5.0
			Bottom	21.6	27.0	27.1	5.36	5.34	5.34	73.4	73.2	73.2	4.08	4.07	4.06	5.0	5.1	5.2
13/05/14	1030-1049	27/Cloudy	Surface	24.1	21.2	21.2	5.57	5.56	5.50	73.8	73.6	73.6	3.26	3.29	3.31	4.2	4.3	
			Middle	23.7	22.1	22.2	5.42	5.44	5.44	72.4	72.6	72.6	3.75	3.77	3.79	4.4	4.7	4.7
			Bottom	23.6	22.6	22.6	5.18	5.20	5.20	69.2	69.4	69.4	4.08	4.07	4.05	5.2	5.2	5.2
15/05/14	1300-1315	28/Cloudy	Surface	25.5	17.4	17.4	5.79	5.78	5.64	78.3	78.1	78.1	3.97	3.94	3.91	5.2	5.1	
			Middle	25.4	17.6	17.6	5.50	5.51	5.51	74.6	74.8	74.8	3.74	3.76	3.78	5.0	4.7	4.9
			Bottom	25.1	18.3	18.3	5.08	5.08	5.08	69.0	70.3	70.3	3.83	3.86	3.89	4.8	5.0	5.2
17/05/14	1430-1445	25/Rainy	Surface	25.9	15.3	15.3	5.86	5.84	5.79	78.9	78.6	78.6	4.92	4.94	4.92	5.8	6.0	
			Middle	25.3	18.8	18.8	5.75	5.73	5.73	77.5	77.3	77.3	5.21	5.23	5.25	6.2	6.3	6.3
			Bottom	25.0	19.2	19.2	5.39	5.37	5.37	72.8	72.5	72.5	5.57	5.56	5.54	6.4	6.7	6.7
20/05/14	1630-1647	25/Cloudy	Surface	25.8	15.3	15.3	5.80	5.78	5.64	78.1	77.8	77.8	5.00	5.02	5.00	6.0	6.1	
			Middle	25.3	18.4	18.4	5.52	5.50	5.50	74.5	74.2	74.2	5.37	5.39	5.37	6.2	6.3	6.3
			Bottom	24.9	19.4	19.5	5.38	5.37	5.37	72.8	72.6	72.6	5.48	5.47	5.45	6.4	6.6	6.6

**Mid-Ebb Tide**

**Monitoring Station : TM-FC2**

Date	Sampling Duration	Ambient Temp (°C) / Weather Condition	Monitoring Depth (m)	Temp (°C)	Salinity (ppt)		Dissolved Oxygen (mg/L)			Dissolved Oxygen Saturation (%)			Turbidity (NTU)			Suspended Solids (mg/L)		
					Value	Average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average	Value	Average	Depth-average
22/05/14	0730-0745	29/Cloudy	Surface	1.0	26.8	18.5	18.5	5.82	5.85	5.63	79.0	79.4	3.00	3.02	4.0			
						18.5		5.88			79.8		3.04			4.0		
						18.7		5.41			73.4		3.46					
	Middle		8.0	26.7	18.7	18.7	5.39	5.40	73.2	73.3	3.49	3.48	3.35	4.4	4.5	4.4		
					18.9		5.27		71.6		3.53			4.6				
					18.9		5.29		72.0		3.57			4.8				
24/05/14	0905-0920	27/Fine	Surface	1.0	26.8	12.3	12.3	5.53	5.54	5.39	73.3	73.5	3.43	3.44	4.3			
						12.2		5.55			73.6		3.45			4.4		
						12.6		5.24			69.6		3.51					
	Middle		8.4	26.8	12.6	12.6	5.23	5.24	69.5	69.6	3.53	3.52	3.51	4.6	4.7	4.6		
					12.8		4.96		65.9		3.56			4.8				
					12.9		4.94		65.7		3.59			4.6				
27/05/14	1100-1117	29/Fine	Surface	1.0	26.9	19.8	19.9	5.75	5.73	5.59	88.1	87.9	5.12	5.14	6.1			
						19.9		5.71			87.6		5.15			6.2		
						22.2		5.47			84.1		5.52					
	Middle		8.2	26.5	22.3	22.3	5.43	5.45	83.5	83.8	5.49	5.51	5.41	6.6	6.5	6.4		
					22.5		5.33		82.1		5.60			6.4				
					22.4		5.30		81.7		5.57			6.8				
29/05/14	1205-1223	33/Fine	Surface	1.0	27.2	19.8	19.9	5.84	5.85	5.68	81.9	82.0	4.96	4.97	5.9			
						19.9		5.86			82.1		4.98			6.0		
						22.3		5.49			77.4		5.54					
	Middle		8.3	26.8	22.4	22.4	5.51	5.50	77.6	77.5	5.56	5.55	5.39	6.6	6.5	6.4		
					22.5		5.34		75.5		5.63			6.6				
					22.5		5.36		75.7		5.65			6.8				
31/05/14	1330-1348	31/Fine	Surface	1.0	27.2	20.0	20.0	5.88	5.87	5.75	82.4	82.3	4.99	5.00	6.1			
						19.9		5.86			82.2		5.01			6.0		
						22.2		5.62			79.3		5.54					
	Middle		8.3	26.8	22.3	22.3	5.64	5.63	79.5	79.4	5.56	5.55	5.40	6.6	6.5	6.5		
					22.4		5.37		75.8		5.63			6.4				
					22.4		5.39		76.0		5.65			6.8				




## **Appendix C3**


### **Graphical Plots of Impact Marine Water Quality Monitoring Data**



### Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

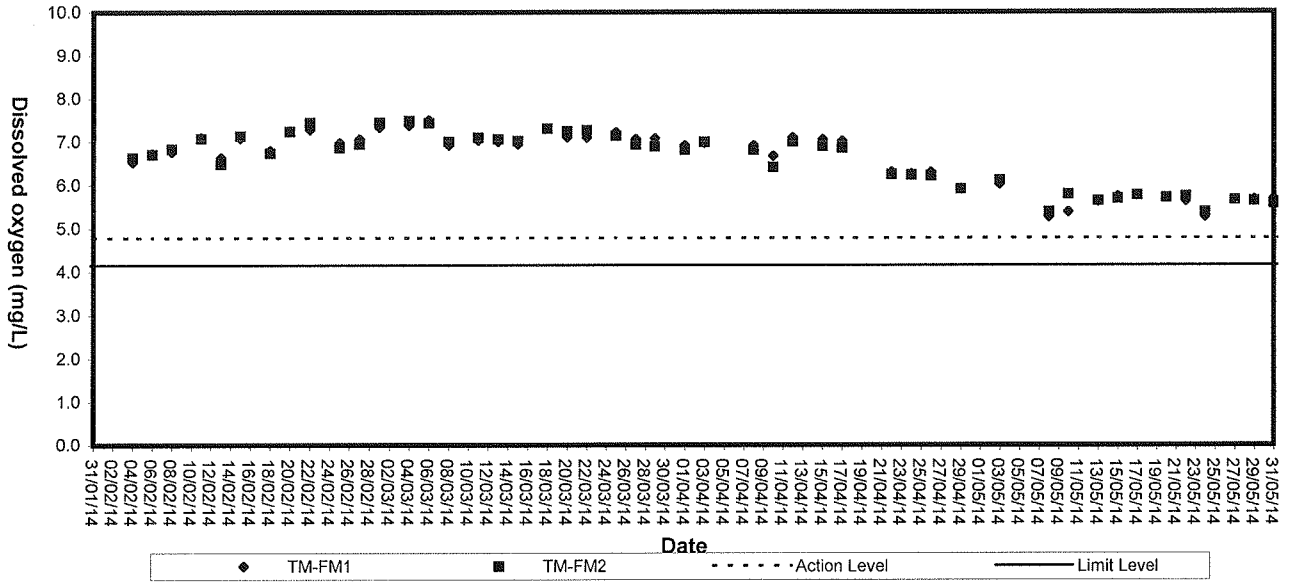


### Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

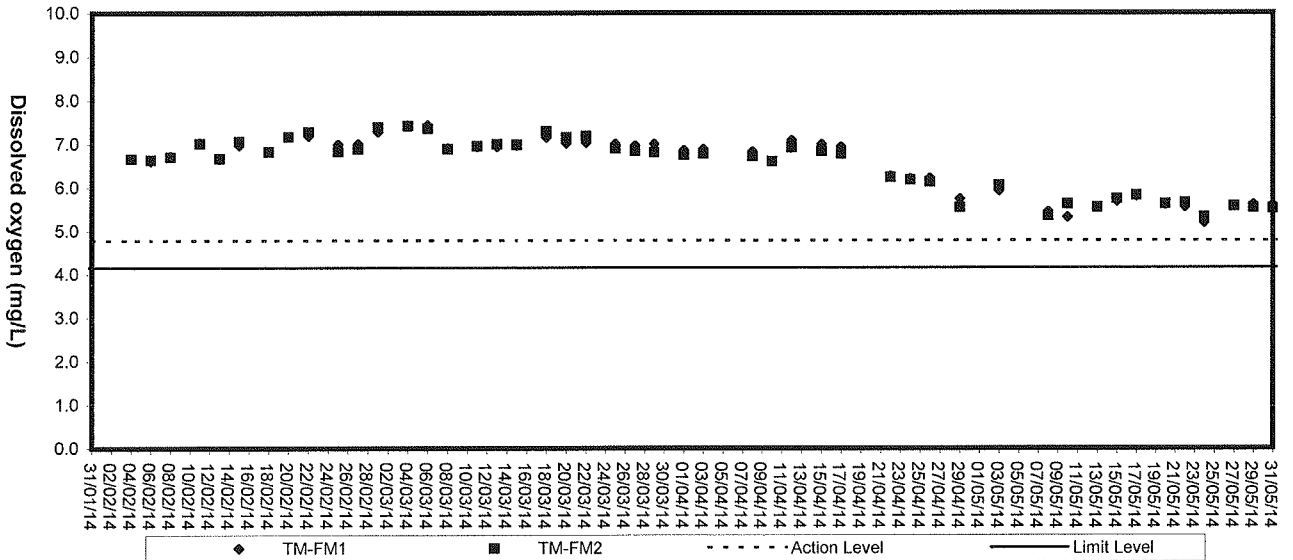






### Dissolved Oxygen (Bottom) at Mid-Flood Tide

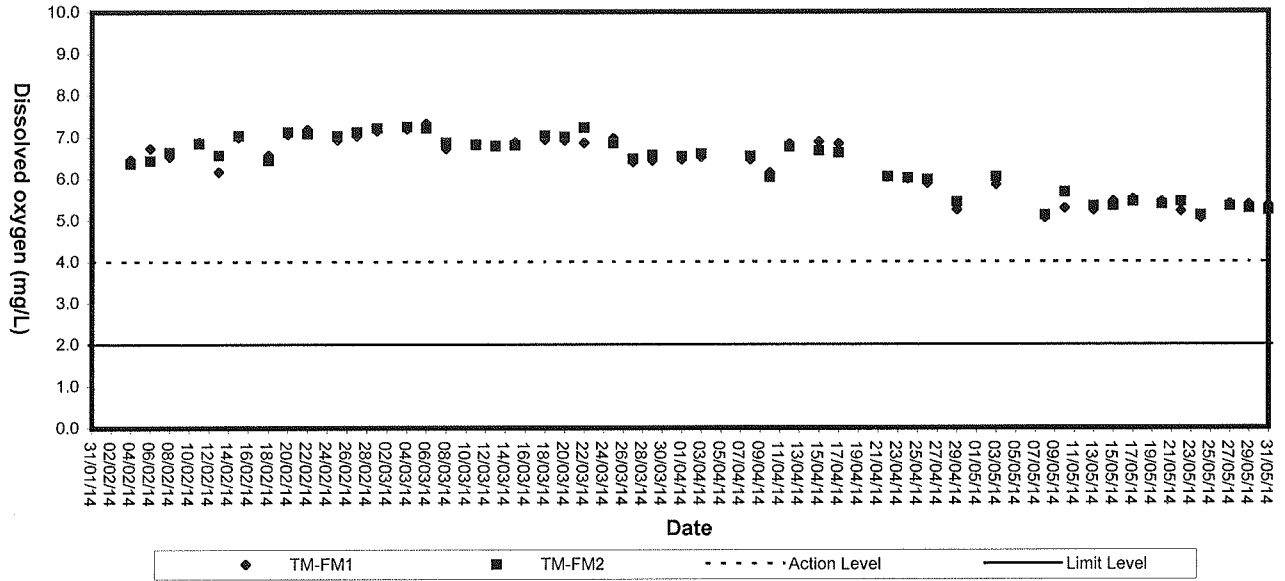


### Dissolved Oxygen (Bottom) at Mid-Ebb Tide

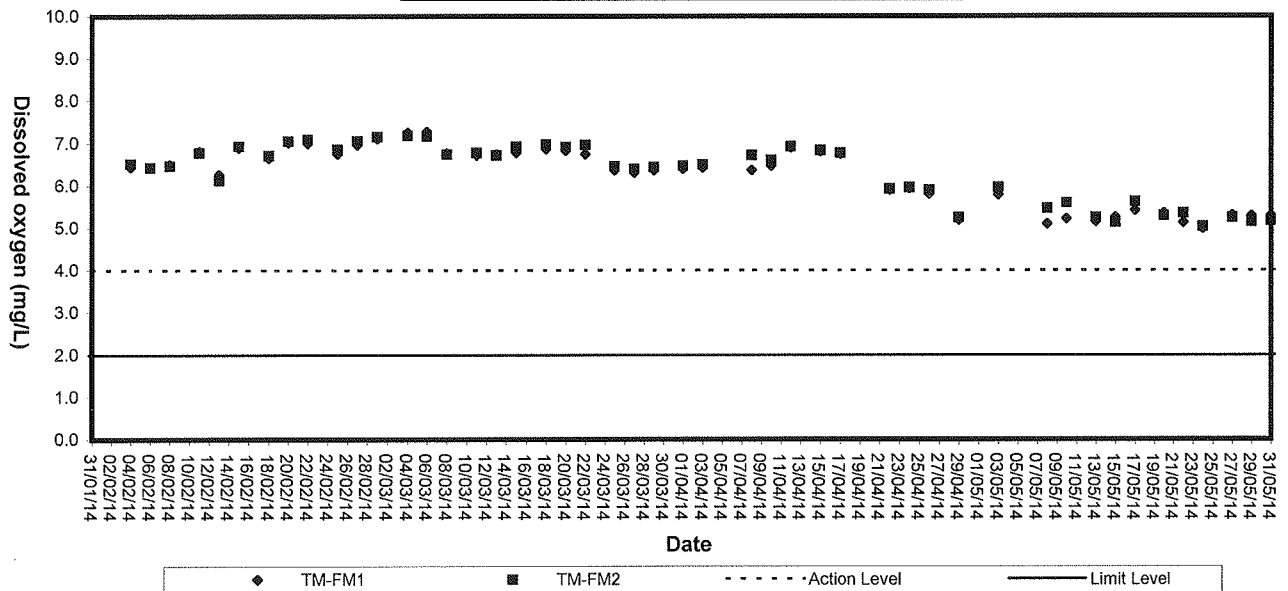




### Turbidity (Depth-average) at Mid-Flood Tide

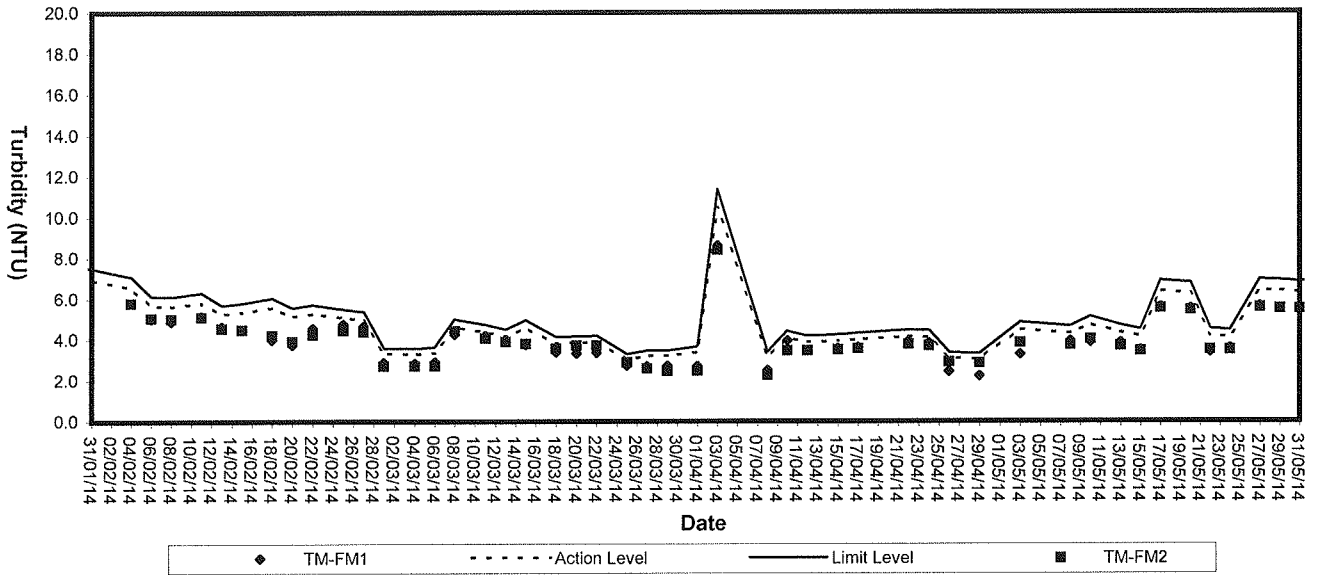


### Turbidity (Depth-average) at Mid-Ebb Tide

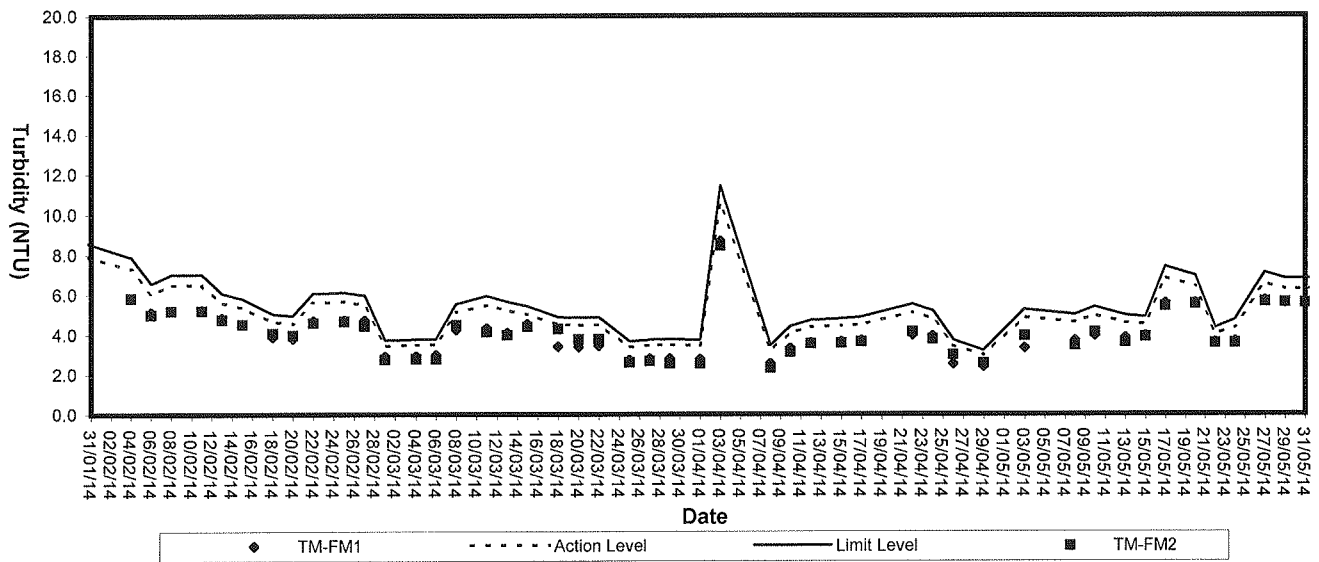




### Suspended solids (Depth-average) at Mid-Flood Tide

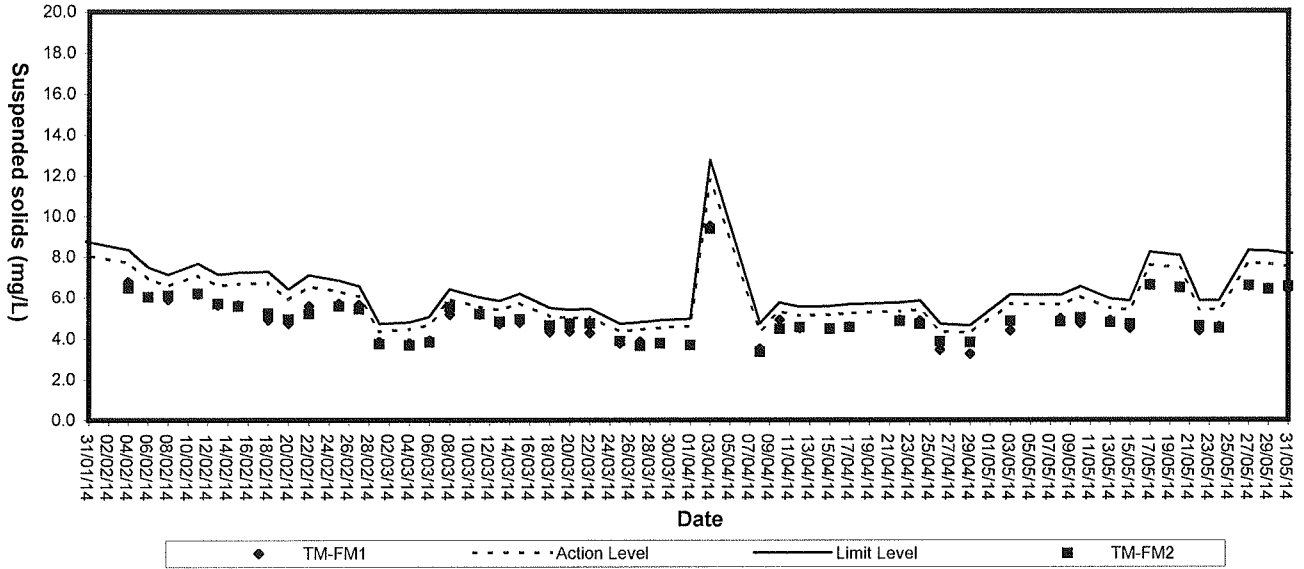

### Suspended Solids (Depth-average) at Mid-Ebb Tide

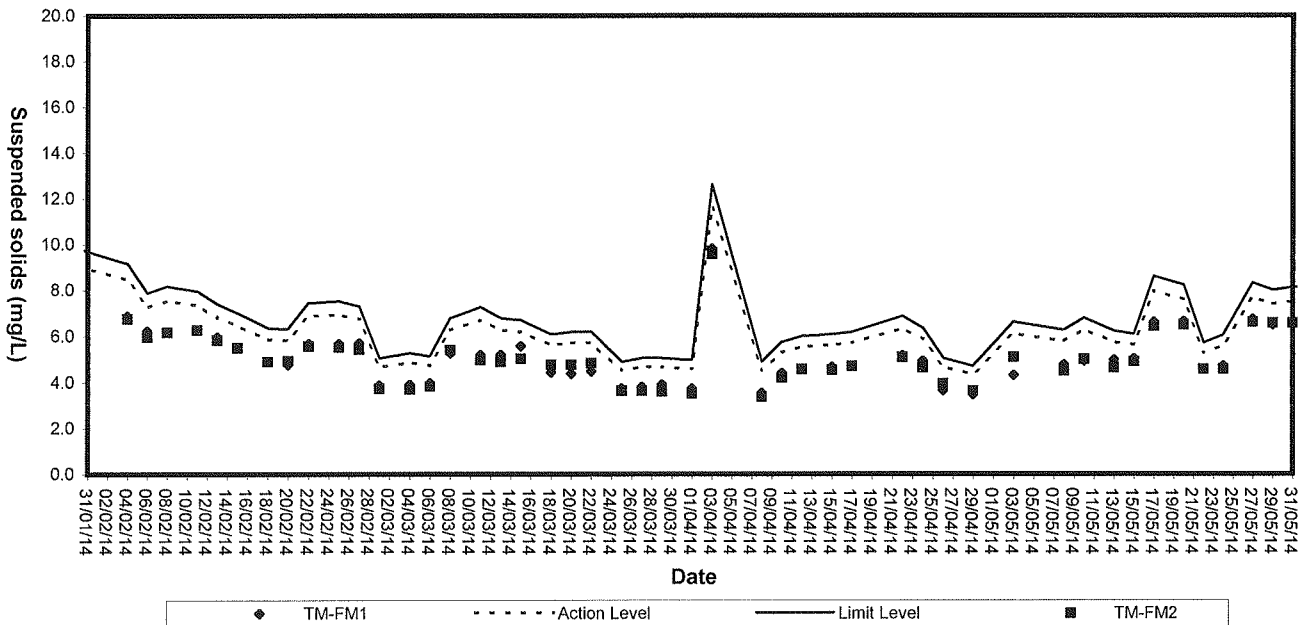



## **Appendix D1**

### **Calibration Certificates for Impact Noise Monitoring Equipments**



Hong Kong Calibration Ltd.

香港校正有限公司

# Calibration Certificate

Page 1 of 3 Pages

Certificate No. 38223

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fofan, Hong Kong.

Order No. : Q33271

Date of receipt : 13-Nov-13

## Item Tested

Description : Precision Integrating Sound Level Meter (ET/EN/003/13)

Manufacturer : Rion

Model : NL-31

Serial No. : 00593620

## Test Conditions

Date of Test : 15-Nov-13

Ambient Temperature : (23 ± 3)°C

Supply Voltage : --

Relative Humidity : (50 ± 25) %

## Test Specifications

Calibration check.

Ref. Document/Procedure : Z01.

## Test Results

All results were within the IEC 651 Type 1 & IEC 804 Type1 specification.  
The results are shown in the attached page(s).

Main Test equipment used:

Equipment No.	Description	Cert. No.	Traceable to
S017	Multi-Function Generator	C127181	SCL-HKSAR
S205	Ref. Sound Level Calibrator	PHCO40002	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).  
The test results apply to the above Unit-Under-Test only

Calibrated by :

Dorothy Cheuk

Approved by :

Steve Kwan

Date: 15-Nov-13

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.



# Calibration Certificate

Certificate No. 38223

Page 2 of 3 Pages

Results :

## 1. SPL Accuracy

UUT Setting			Applied Value (dB)	UUT Reading (dB)
Level Range (dB)	Weight	Response		
20 - 100	L <sub>A</sub>	Fast	94.0	94.0
		Slow		94.0
	L <sub>C</sub>	Fast		94.0
	L <sub>p</sub>	Fast		94.0
30 - 120	L <sub>A</sub>	Fast	94.0	94.0
		Slow		94.0
	L <sub>C</sub>	Fast		94.0
	L <sub>p</sub>	Fast		94.0
30 - 120	L <sub>A</sub>	Fast	114.0	114.0
		Slow		114.0
	L <sub>C</sub>	Fast		114.0
	L <sub>p</sub>	Fast		114.0

IEC 651 Type 1 Spec. :  $\pm 0.7$  dB  
Uncertainty :  $\pm 0.1$  dB

2. **Level Stability** : 0.0 dB  
IEC 651 Type 1 Spec. :  $\pm 0.3$  dB  
Uncertainty :  $\pm 0.01$  dB

## 3. Linearity

### 3.1 Level Linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec. (Primary Indicator Range)
130	114.0	114.0	0.0	$\pm 0.7$ dB
130	104.0	104.0	0.0	
120	94.0	94.0 (Ref.)	--	
110	84.0	84.0	0.0	
100	74.0	74.0	0.0	
90	64.0	64.1	0.1	
80	54.0	54.1	0.1	

Uncertainty :  $\pm 0.1$  dB



# Calibration Certificate

Certificate No. 38223

Page 3 of 3 Pages

### 3.2 Differential level linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec.
120	84.0	84.0	0.0	± 0.4 dB
	94.0	94.0 (Ref.)	--	
	95.0	95.0	0.0	± 0.2 dB

Uncertainty : ± 0.1 dB

### 4. Frequency Weighting - A weighting

Frequency	Attenuation (dB)	IEC 651 Type 1 Spec.
31.5 Hz	39.6	- 39.4 dB, ± 1.5 dB
63 Hz	-36.3	- 26.2 dB, ± 1.5 dB
125 Hz	-16.3	- 16.1 dB, ± 1 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1 dB
1 kHz	0.0 (Ref.)	0 dB, ± 1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1 dB
4 kHz	+1.1	+ 1.0 dB, ± 1 dB
8 kHz	-1.0	- 1.1 dB, + 1.5 dB ~ - 3 dB
16 kHz	-6.4	- 6.6 dB, + 3 dB ~ - ∞

Uncertainty : ± 0.1 dB

### 5. Time Averaging

6.

Applied Burst duty Factor	Applied Leq Value (dB)	UUT Reading (dB)	IEC 804 Type 1 Spec.
continuous	40.0	40.0	--
1/10	40.0	39.9	± 0.5 dB
1/10 <sup>2</sup>	40.0	39.7	
1/10 <sup>3</sup>	40.0	39.8	± 1.0 dB
1/10 <sup>4</sup>	40.0	39.8	

Uncertainty : ± 0.1 dB

- Remarks:
1. UUT : Unit-Under-Test
  2. The uncertainty claimed is for a confidence probability of not less than 95%.
  3. Atmospheric Pressure : 1006 hPa
  4. The UUT was adjusted with the supplied sound calibrator at the reference sound pressure level before the calibration.

----- END -----



# Calibration Certificate

Certificate No. **38224**

Page 1 of 2 Pages

**Customer :** ETS-Testconsult Limited

**Address :** 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

**Order No. :** Q33271

**Date of receipt :** 13-Nov-13

## Item Tested

**Description :** Sound Level Calibrator (ET/EN/002/01)

**Manufacturer :** Rion

**Model :** NC-73

**Serial No. :** 10196943

## Test Conditions

**Date of Test :** 15-Nov-13

**Supply Voltage :** --

**Ambient Temperature :** (23 ± 3)°C

**Relative Humidity :** (50 ± 25) %

## Test Specifications

Calibration check.

Ref. Document/Procedure : F21, Z02.

## Test Results

All results were within the manufacturer's specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	35730	NIM-PRC & SCL-HKSAR
S205	Ref. Sound Level Calibrator	PHCO40002	SCL-HKSAR
S041	Universal Counter	34621	SCL-HKSAR
S206	Sound Level Meter	36203	SCL-HKSAR
S031	6½ dgt. Multimeter	30128	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

Calibrated by : Dorothy Cheuk  
Dorothy Cheuk

Approved by : Steve Kwan  
Steve Kwan

Date: 15-Nov-13

This Certificate is issued by:  
Hong Kong Calibration Ltd.  
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.  
Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.





# Calibration Certificate

Certificate No. 38224

Page 2 of 2 Pages

Results :

## 1. Level Accuracy (at 1 kHz)

UUT Nominal Value	Measured Value	Mfr's Spec.
94 dB	94.1 dB	$\pm 1$ dB

Uncertainty :  $\pm 0.2$  dB

## 2. Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's Spec.
1 kHz	0.986 kHz	$\pm 2$ %

Uncertainty :  $\pm 0.1$  %

## 3. Level Stability : 0.0 dB

Uncertainty :  $\pm 0.01$  dB

## 4. Total Harmonic Distortion : $< 0.1$ %

Mfr's Spec. :  $< 3$  %

Uncertainty :  $\pm 2.3$  % of reading

Remarks: 1. UUT : Unit-Under-Test  
2. The uncertainty claimed is for a confidence probability of not less than 95%.  
3. Atmospheric Pressure : 1006 hPa

----- END -----



## **Appendix D2**

### **Impact Noise Monitoring Results**



## Day-time Noise Monitoring`

### Monitoring Location: TM-RN1 \*

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L <sub>eq(30min)</sub>	L <sub>10</sub>	L <sub>90</sub>		
03/05/14	11:36	55.6	57.9	53.2	0.4	Fine
08/05/14	09:05	57.4	59.0	52.8	0.3	Cloudy
10/05/14	14:33	57.6	58.8	54.1	0.4	Cloudy
13/05/14	13:00	56.7	58.0	52.9	0.4	Cloudy
15/05/14	13:00	57.2	58.8	52.9	0.4	Drizzle
22/05/14	08:25	57.1	59.0	52.7	0.3	Cloudy
24/05/14	13:00	56.8	59.3	51.4	0.3	Fine
27/05/14	09:15	57.2	58.8	52.1	0.4	Fine
29/05/14	08:33	58.6	59.2	53.8	0.3	Fine

Remark: Since Lands Department did not approve us to enter their own area where the noise monitoring stations TM-N1 and TM-N2 located due to the security, noise monitoring was carried out at noise monitoring stations TM-RN1 and TM-RN2 (refer to the figure 3 attached) in this reporting month.

### Monitoring Location: TM-RN2 \*

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L <sub>eq(30min)</sub>	L <sub>10</sub>	L <sub>90</sub>		
03/05/14	11:39	56.1	58.4	52.8	0.5	Fine
08/05/14	09:10	57.7	59.5	53.2	0.4	Cloudy
10/05/14	14:36	56.6	58.9	52.7	0.4	Cloudy
13/05/14	13:05	57.4	58.8	52.6	0.5	Cloudy
15/05/14	13:05	57.6	59.1	52.5	0.3	Drizzle
22/05/14	08:30	58.4	59.6	53.2	0.3	Cloudy
24/05/14	13:02	57.5	59.4	52.5	0.3	Fine
27/05/14	09:20	58.0	59.4	53.0	0.3	Fine
29/05/14	08:36	57.2	58.4	52.9	0.3	Fine

Remark: Since Lands Department did not approve us to enter their own area where the noise monitoring stations TM-N1 and TM-N2 located due to the security, noise monitoring was carried out at two noise monitoring stations TM-RN1 and TM-RN2 (refer to the figure 3 attached) in this reporting month.




## **Appendix D3**

### **Graphical Plots of Impact Noise Monitoring Data**



## Noise Monitoring (Day-time)

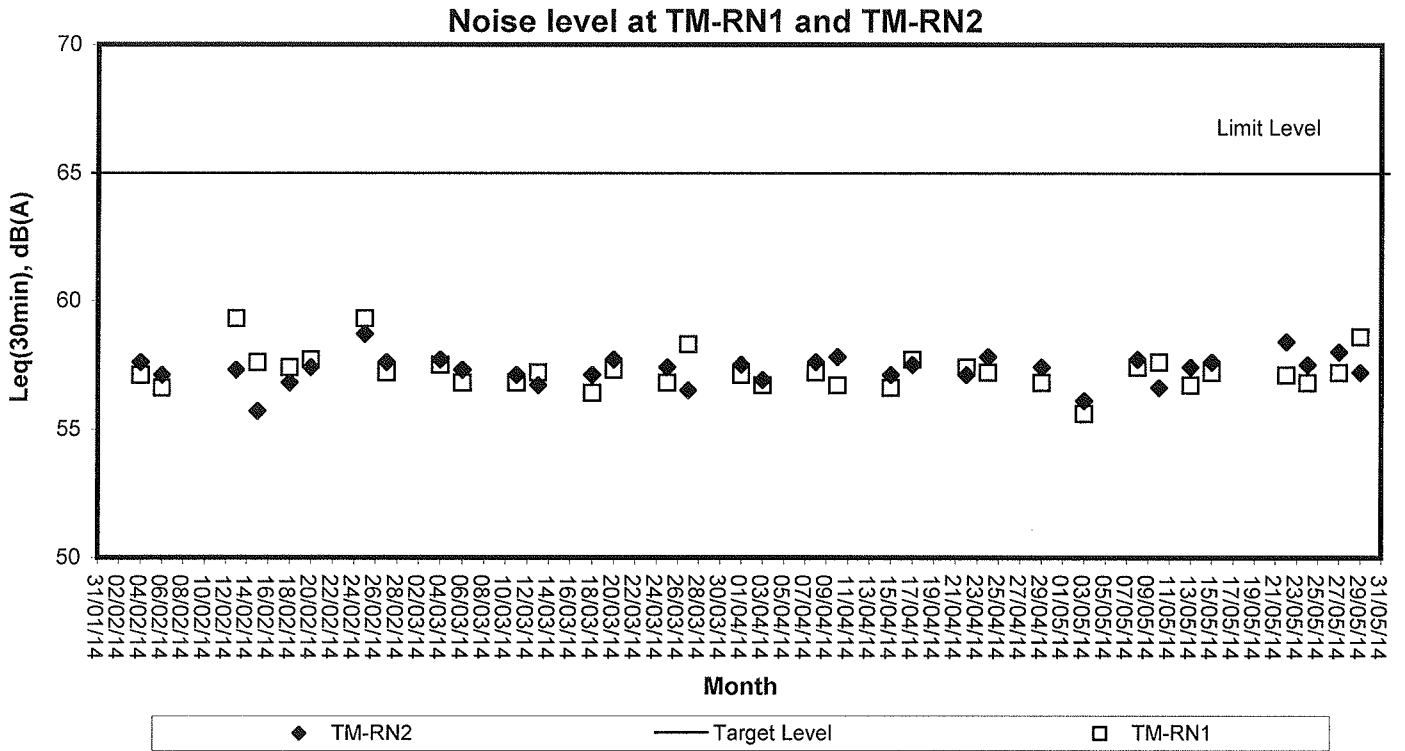



## **Appendix E**

### **Weather Condition**

## Extract of Meteorological Observations for Tuen Mun Automatic Weather Station, May 2014

Date	Mean Pressure at M.S.L. (hPa)	Air Temperature			Mean Dew Point Temperature (deg C)	Relative Humidity		
		Max. (deg C)	Mean (deg C)	Min. (deg C)		Max. (%)	Mean (%)	Min. (%)
May 1	*****	26.6	23.3	21.3	20.5	96	84	72
May 2	*****	28.4	24.7	22.0	20.2	88	76	61
May 3	*****	30.7	25.9	22.9	18.8	83	66	46
May 4	*****	24.4	23.5	22.1	21.5	97	89	79
May 5	*****	25.5	21.6	18.9	19.4	98	88	66
May 6	*****	20.4	19.3	18.7	18.3	97	94	85
May 7	*****	21.3	20.5	19.5	19.4	97	94	90
May 8	*****	24.8	22.7	20.8	21.8	99	95	85
May 9	*****	22.3	21.7	21.2	21.4	99	98	95
May 10	*****	27.4	24.0	21.9	22.3	99	90	76
May 11	*****	25.9	23.8	22.2	23.0	100	95	85
May 12	*****	29.8	26.1	23.2	24.3	100	90	73
May 13	*****	30.8	27.8	25.3	25.6	99	88	75
May 14	*****	30.9	28.6	26.9	25.4	92	83	73
May 15	*****	32.0	29.1	27.3	26.1	95	84	71
May 16	*****	30.1	27.9	25.8	26.4	98	92	81
May 17	*****	31.6	28.2	25.9	26.2	99	90	73
May 18	*****	31.3	28.2	26.4	25.9	96	88	75
May 19	*****	32.2	28.3	24.1	25.6	98	86	69
May 20	*****	31.9	26.6	22.9	25.2	99	92	72
May 21	*****	29.9	26.9	23.9	24.9	99	89	78
May 22	*****	30.4	28.8	27.4	25.5	92	83	76
May 23	*****	28.3	26.9	24.7	25.6	97	93	87
May 24	*****	32.0	28.4	25.8	25.8	94	86	73
May 25	*****	33.4	28.9	24.0	25.7	100	84	65
May 26	*****	32.5	29.5	26.9	26.0	94	82	67
May 27	*****	33.5	29.8	27.4	26.1	91	81	63
May 28	*****	32.9	29.4	27.3	25.5	90	80	67
May 29	*****	32.5	29.4	27.1	25.9	94	82	64
May 30	*****	33.0	29.9	27.4	26.0	91	80	66
May 31	*****	34.4	30.3	27.0	26.1	93	79	62
<b>Mean</b>	*****	29.4	26.5	24.1	23.9	96	86	73
<b>Maximum</b>	*****	34.4	30.3	27.4	26.4	100	98	95
<b>Minimum</b>	*****	20.4	19.3	18.7	18.3	83	66	46

## Extract of Meteorological Observations for Tuen Mun Automatic Weather Station, May 2014

Date	Total Rainfall (mm)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
May 1	0.0	***	*****
May 2	0.0	***	*****
May 3	0.0	***	*****
May 4	12.5	***	*****
May 5	45.0	***	*****
May 6	3.5	***	*****
May 7	4.0	***	*****
May 8	57.0	***	*****
May 9	78.0	***	*****
May 10	3.0	***	*****
May 11	134.5	***	*****
May 12	6.5	***	*****
May 13	15.5	***	*****
May 14	0.0	***	*****
May 15	0.0	***	*****
May 16	19.5	***	*****
May 17	29.0	***	*****
May 18	2.5	***	*****
May 19	9.5	***	*****
May 20	44.5	***	*****
May 21	12.0	***	*****
May 22	0.5	***	*****
May 23	8.0	***	*****
May 24	0.0	***	*****
May 25	29.0	***	*****
May 26	0.0	***	*****
May 27	0.0	***	*****
May 28	0.0	***	*****
May 29	0.0	***	*****
May 30	0.0	***	*****
May 31	0.0	***	*****
<b>Mean</b>	-----	***	*****
<b>Total</b>	514.0	---	-----
<b>Maximum</b>	134.5	---	*****
<b>Minimum</b>	0.0	---	*****

\*\*\* unavailable

# missing (less than 24 hourly observations a day)

Rainfall measured in increment of 0.5 mm. Amount of < 0.5 mm cannot be detected





## **Appendix F**

### **Event-Action Plans**

## EVENT/ACTION PLAN FOR AIR QUALITY EXCEEDANCE

ACTION

	ET Leader	IC(E)	ER	Contractor
	<b>ACTION LEVEL</b>			
1. Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures</li> <li>2. Inform ER, IC(E) and Contractor</li> <li>3. Repeat measurement to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by the ET</li> <li>2. Check contractor's working method</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practise</li> <li>2. Amend working methods if appropriate</li> </ol>
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures</li> <li>2. Inform IC(E) and Contractor</li> <li>3. Repeat measurements to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> <li>5. Discuss with IC(E) and Contractor on remedial actions</li> <li>6. If exceedance continues, arrange meeting with IC(E) and ER.</li> <li>7. If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by the ET</li> <li>2. Check Contractor's working method</li> <li>3. Discuss with ET and Contractor on possible remedial measures</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures</li> <li>5. Supervise implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Notify the Contractor</li> <li>3. Ensure remedial measures properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>2. Implement the agreed proposals</li> <li>3. Amend proposal if appropriate</li> </ol>
	<b>LIMIT LEVEL</b>			
1. Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures</li> <li>2. Inform ER, Contractor and EPD</li> <li>3. Repeat measurement to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> <li>5. Assess the effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by the ET</li> <li>2. Check Contractor's working method</li> <li>3. Discuss with ET and Contractor on possible remedial measures</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures</li> <li>5. Supervise implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Notify the Contractor</li> <li>3. Ensure remedial measures properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>3. Implement the agreed proposals</li> <li>4. Amend proposal if appropriate.</li> </ol>

## EVENT/ACTION PLAN FOR AIR QUALITY EXCEEDANCE

EVENT	ACTION			Contractor
	ET Leader	IC(E)	ER	
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures</li> <li>2. Notify IC(E), ER, EPD and Contractor</li> <li>3. Repeat measurement to confirm finding</li> <li>4. Increase monitoring frequency to daily</li> <li>5. Carry out analysis of contractor's working procedures to determine possible mitigation to be implemented</li> <li>6. Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</li> <li>8. If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET and Contractor on the potential remedial actions</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly</li> <li>3. Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing</li> <li>2. Notify Contractor</li> <li>3. In consultation with the IC(E), agree with the Contractor on the remedial measures to be implemented</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. If exceedances continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedances</li> <li>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification</li> <li>3. Implement the agreed proposals</li> <li>4. Resubmit proposals if problem still not under control</li> <li>5. Stop the relevant activity of works as determined by the ER until the exceedance is abated</li> </ol>

## EVENT/ACTION PLAN FOR NOISE EXCEEDANCE

EVENT	ACTION			
	ET Leader	IC(E)	ER	Contractor
Action Level	<ol style="list-style-type: none"> <li>1. Notify the IC(E) and the Contractor.</li> <li>2. Carry out investigation.</li> <li>3. Report the results of investigation to the IC(E) and the Contractor.</li> <li>4. Discuss with the Contractor and formulate remedial measures.</li> <li>5. Increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analysed results submitted by the ET.</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly.</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing.</li> <li>2. Notify the Contractor.</li> <li>3. Require the Contractor to propose remedial measures for the analysed noise problem.</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IC(E).</li> <li>2. Implement noise mitigation proposals.</li> </ol>
Limit Level	<ol style="list-style-type: none"> <li>1. Notify the IC(E), the ER, the EPD and the Contractor.</li> <li>2. Identify source.</li> <li>3. Repeat measurement to confirm findings.</li> <li>4. Increase monitoring frequency.</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>6. Inform the IC(E), the ER and the EPD the causes &amp; actions taken for the exceedances.</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep the IC(E), the EPD and the ER informed of the results</li> <li>8. If exceedance due to the construction works stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst the ER, the ET Leader and the Contractor on the potential remedial actions.</li> <li>2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing.</li> <li>2. Notify the Contractor.</li> <li>3. Require the Contractor to propose remedial measures for the analysed noise problem.</li> <li>4. Ensure remedial measures are properly implemented.</li> <li>5. If exceedances continue, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedances is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance</li> <li>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification.</li> <li>3. Implement the agreed proposals.</li> <li>4. Resubmit proposals if problem still not under control.</li> <li>5. Stop the relevant activity of works as determined by the ER until the exceedances is abated.</li> </ol>

## EVENT AND ACTION PLAN FOR WATER QUALITY EXCEEDANCE

Event	ACTION			IEC
	ET Leader	Contractor	ER	
<p>Action level being exceeded by one sampling day</p>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Repeat in-situ measurement to confirm findings;</li> <li>3. Notify Contractor in writing within 24 hours of identification of the exceedance</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Carry out investigation</li> <li>6. Report the results of investigation to the Contractor within 3 working days of identification of exceedance and advise contractor if exceedance is due to contractor's construction works</li> <li>7. Discuss mitigation measures with Contractor if exceedance is due to the construction works within 4 working days</li> <li>8. Repeat measurement on next day of exceedance if exceedance is due to the construction works</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify the ER and IEC in writing within 24 hours of identification of exceedance</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Submit investigation report to IEC and ER within 3 working days of the identification of an exceedance</li> <li>5. Consider changes of working method if exceedance is due to the construction works</li> <li>6. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER if exceedance is due to the construction works within 4 working days of identification of an exceedance</li> <li>7. Implement the agreed mitigation measures within reasonable time scale</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify EPD and other relevant governmental agencies in writing within 24 hours of the identification of the exceedance</li> <li>2. Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>3. Require contractor to propose remedial measures for the analysed problem if related to the construction works</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. Assess the effectiveness of the mitigation measure</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET</li> <li>2. Confirm ET assessment if exceedance is due / not due to the works</li> <li>3. Discuss with ET, ER and Contractor on the mitigation measures</li> <li>4. Review contractor's mitigation measures whenever necessary to ensure their effectiveness and advise the ER accordingly</li> <li>5. Supervise the implementation of mitigation measures</li> </ol>

## EVENT AND ACTION PLAN FOR WATER QUALITY

Event	ACTION			
	ET Leader	Contractor	ER	IEC
<p>Action level being exceeded by more than one consecutive sampling days</p>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Repeat in-situ measurement to confirm findings</li> <li>3. Notify Contractor in writing within 24 hours of identification</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Carry out investigation</li> <li>6. Report the results of investigation to the Contractor within 3 working days of identification of exceedance and advise contractor if exceedance is due to contractor's construction works</li> <li>7. Discuss mitigation measures with IEC and Contractor within 4 working of identification of an exceedance</li> <li>8. Ensure mitigation measures are implemented;</li> <li>9. Prepare to increase the monitoring frequency to daily;</li> <li>10. Repeat measurement on next day of exceedance.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify IEC and ER in writing within 24 hours of identification of exceedance</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Submit the results of the investigation to IEC and ER within 3 working days of the identification of an exceedance</li> <li>6. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 4 working days of identification of an exceedance</li> <li>7. Implement the agreed mitigation measures within reasonable time scale</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify EPD and other relevant governmental agencies in writing within 24 hours of the identification of the exceedance</li> <li>2. Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>3. Require contractor to propose remedial measures for the analysed problem if related to the construction works</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. Assess the effectiveness of the mitigation measure</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET</li> <li>2. Confirm ET assessment if exceedance is due / not due to the works</li> <li>3. Discuss with ET, ER and Contractor on the mitigation measures.</li> <li>4. Review contractor's mitigation measures whenever necessary to ensure their effectiveness and advise the ER accordingly</li> <li>5. Assess the effectiveness of the implemented mitigation measures.</li> </ol>


## EVENT AND ACTION PLAN FOR WATER QUALITY EXCEEDANCE

Event	ACTION			IEC
	ET Leader	Contractor	ER	
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurement to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Notify Contractor in writing within 24 hours of identification of the exceedance</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Carry out investigation</li> <li>6. Report the results of investigation to the Contractor within 3 working days of identification of exceedance and advise contractor if exceedance is due to contractor's construction works</li> <li>7. Discuss mitigation measures with IEC, ER and Contractor within 4 working of identification of an exceedance</li> <li>8. Ensure mitigation measures are implemented;</li> <li>9. Increase the monitoring frequency to daily until no exceedance of Limit Level.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify IEC and ER in writing; within 24 hours of the identification of the exceedance</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>5. Submit the results of the investigation to IEC and ER within 3 working days of the identification of an exceedance</li> <li>6. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 4 working days of the identification of an exceedance</li> <li>7. Implement the agreed mitigation measures within reasonable time scale</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify EPD and other relevant governmental agencies in writing within 24 hours of identification of exceedance</li> <li>2. Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>3. Request Contractor to critically review the working methods;</li> <li>4. Ensure remedial measures are properly implemented</li> <li>5. Assess the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET</li> <li>2. Confirm ET assessment if exceedance is due / not due to the works</li> <li>3. Discuss with ET, ER and Contractor on the mitigation measures.</li> <li>4. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly.</li> <li>5. Assess the effectiveness of the implemented mitigation measures</li> </ol>

## EVENT AND ACTION PLAN FOR WATER QUALITY EXCEEDANCE

Event	ACTION		
	ET Leader	Contractor	IEC
Limit Level being exceeded by more than one consecutive sampling days	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurement to confirm findings;</li> <li>2. Identify source(s) of impact;</li> <li>3. Notify Contractor in writing within 24 hours of identification of the exceedance</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>5. Carry out investigation</li> <li>6. Report the results of investigation to the Contractor within 3 working days of identification of exceedance and advise contractor if exceedance is due to contractor's construction works</li> <li>7. Discuss mitigation measures with IEC, ER and Contractor;</li> <li>8. Ensure mitigation measures are implemented;</li> <li>9. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify ER and IEC in writing within 24 hours of the identification of the exceedance and</li> <li>2. Rectify unacceptable practice;</li> <li>3. Check all plant and equipment;</li> <li>4. Consider changes of working methods;</li> <li>8. Submit the results of the investigation to IEC and ER within 3 working days of the identification of an exceedance</li> <li>5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 4 working days;</li> <li>6. Implement the agreed mitigation measures within reasonable time scale</li> <li>7. As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify EPD and other relevant governmental agencies in writing within 24 hours of identification of exceedance</li> <li>2. Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>3. Request Contractor to critically review the working methods;</li> <li>6. Ensure remedial measures are properly implemented</li> <li>4. Assess the effectiveness of the implemented mitigation measures;</li> <li>5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level.</li> </ol>
			<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET</li> <li>2. Confirm ET assessment if exceedance is due / not due to the works</li> <li>3. Discuss with ER, ET and Contractor on the mitigation measures.</li> <li>4. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly.</li> <li>5. Assess the effectiveness of the implemented mitigation measures.</li> </ol>



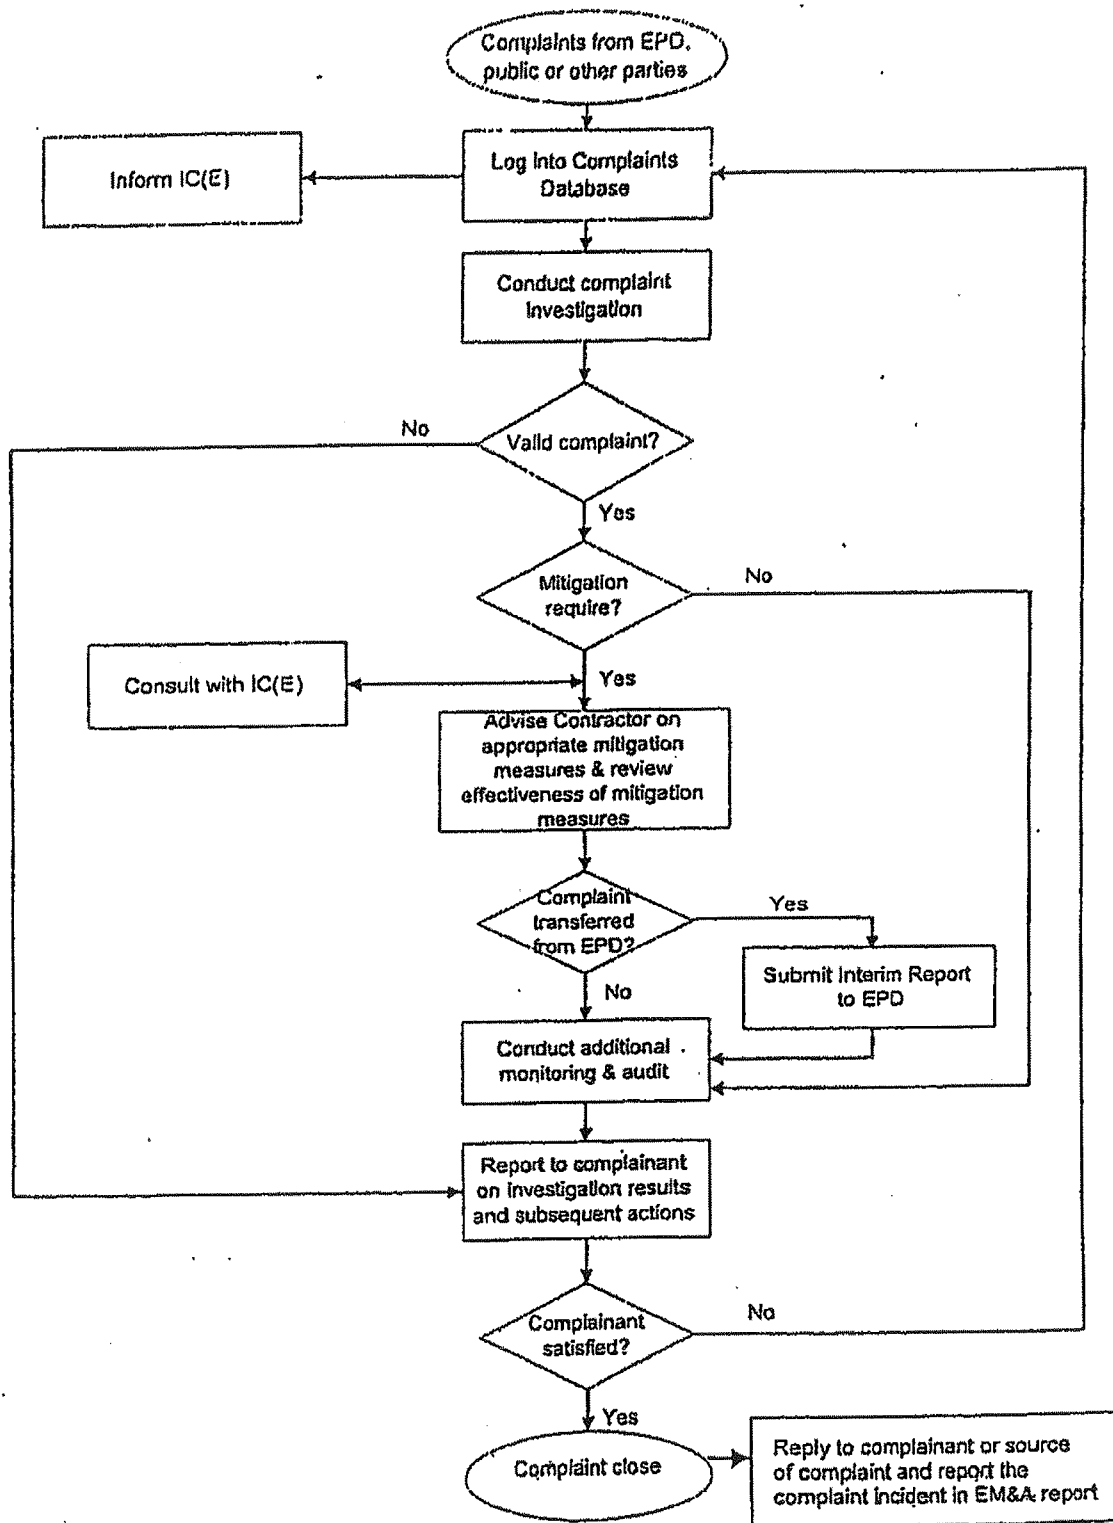

Contract No. CV/2013/06  
 Handling of Surplus Public Fill (2014-2016)

Figure 4  
 Environmental Complaint Handling Procedure –  
 Tuen Mun Area 38 Fill Bank



東業德勤測試顧問有限公司  
 ETS-TESTCONSULT LIMITED

## **Appendix G**

### **Construction Programme**

Master Programme of Contract No. CV/2013/06 - Handling of Surplus Public Fill

Site Location : Tuen Mun Area 38 Fill Bank

ID	Activity	Original Duration	Start	Finish
A1240	Take Over	0	23-Jan-14	
A1220	Operation	1100	23-Jan-14	26-Jan-17
A1250	Hand Over to CEDD	0		26-Jan-17
Stage B1 Surveillance System		120	28-Nov-13	27-May-14
A1190	Submission	30	28-Nov-13	27-Dec-13
A1200	Approval by Engineer	7	28-Dec-13	03-Jan-14
A1210	Installation	64	23-Jan-14	27-May-14
A1230	Hand Over to Engineer	0		27-May-14






## **Appendix H**

### **Weekly ET's Site Inspection Record**



CEDD Contract No.: CV2013/06  
Handling of Surplus Public Fill(2014-2016) - Tuen Mun Area 38 Fill Bank

Inspection Date : 8/5/14  
 Time : 10:00  
 Weather : Sunny / Fine / Cloudy / Overcast / Drizzle / Rain / Storm / Hazy  
 Wind : Calm / Light / Breeze / Strong  
 Temperature : 21°C  
 Humidity : High / Moderate / Low

Inspected by	CEDD	Contractor / Sub-Contractor	ET
Signature:			
Name:	WONG K. KING	P. Van Uen	Mak Kai Wai
Title	LOW/P3	Sub-Contractor	E.T



Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Fugitive Dust Emission</b>				
▪ Dust control / mitigation measures shall be provided to prevent dust nuisance.	√			
▪ Water sprays shall be provided and used to dampen materials.	√			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	√			
▪ Any vehicle with open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards. Material having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.	√			
▪ Unpaved areas should be watered regularly to avoid dust generation.	√			
▪ The designated site main haul road shall be paved or regular watering.	√			
▪ The haul road inside the site and public road around the site entrance should be kept clean and free from dust.	√			
▪ Wheel washing facilities including high-pressure water jet shall be provided at the entrance of work site.	√			
▪ Every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving the fill bank.	√			
▪ The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	√			
▪ Vehicle and equipment should be switched off while not in use.	√			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	√			
▪ Open burning should be prohibited.	√			
<b>Noise Impact</b>				
▪ The approved method of working, equipment and sound-reducing measures (e.g. use of silenced type of equipment, etc.) shall be adapted.	√			
▪ The constructions works should be scheduled to minimize noise nuisance.	√			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	√			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	√			
▪ Air compressors and hand held breakers should have noise labels.	√			
▪ Compressors and generators should operate with door closed.	√			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	√			
▪ Noisy equipment and mobile plant shall always be site away from NSRs.	√			



Environmental Checklist	Implementation Stages*		Remark
	Yes	No / N/A	
<b>Water Quality</b>			
Drainage system and the sand / silt removal facilities should be adequate and well maintained to prevent flooding and overflow, especially after rain storms.	✓		
The storm water intercepting system shall be effective to collect of runoff and remove suspended solids before discharge.	✓		
Unnecessary water retained in receptacles and standing water should be avoided to prevent mosquito breeding.	✓		
The material shall be properly covered to prevent washed away especially before rainstorm.	✓		
The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	✓		
Final slope surfaces, especially those facing to the north of the site shall be treated by compaction, followed by hydroseeding, vegetation planting or sealing with shotconcrete, latex, vinyl, bitumen, or other suitable surface stabilizer approved by CEDD.	✓		
Existing and newly constructed Catchpits, sand and silt removal facilities and intercepting channels shall be maintained, and the deposited silt and grit shall be removed weekly and on a need basis especially at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	✓		
A wheel washing bay shall be provided at the site exit and wash-water shall have sand and silt settled out or removed before being discharged into storm drains.	✓		
The section of construction road between wheel washing bay and the public road shall be paved with concrete, bituminous materials or hardcore to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.	✓		
Sewage from toilets shall be discharged in to a foul sewer, or chemical toilets shall be provided.	✓		
The chemical toilets (if use) shall be provided by a licensed contractor, who will be responsible for disposal and maintenance of these facilities.	✓		
Tipping halls enclosed with top and 3-side to prevent spillage of material into marine water.	✓		
The barges shall be in right size such that adequate clearance is maintained between the vessels and the seabed at all states of the tide to ensure the undue turbidity is not generated by turbulence from vessel movement or propeller wash.	✓		
All vessels used for transportation of fill material shall have tight fitting seals to their bottom openings to prevent leakage of material during transport.	✓		
Barges shall not be filled to a level which may cause the overflow of material during loading or transportation. Barge effluents shall be properly collected and treated before disposal.	✓		
Adequate environmental control measures shall be provided to prevent / avoid dropping of fill material into the sea during the transfer.	✓		
The work activities shall not cause any visible foam, oil, grease, scum, litter or other objectionable matters to be present on the water in the vicinity of the barging facilities.	✓		
A waste collection vessel shall be deployed to remove floating debris.	✓		
<b>Landscape and Visual</b>			
The maximum stockpiling height at the fill bank shall be limited to a maximum of +40mPD.	✓		
Surface of outer slopes of the Fill Bank shall preferably be hydroseeded.	✓		
Stockpile of public fill shall be removed in a sequence to allow the outer hydroseeded to be removed later than other portions as far as practicable.	✓		
Casuarina equisetifolia were planted as buffer tree along the northern perimeter of the Site. The height of Casuarina equisetifolia was maintained at least 3m above soil level.	✓		
Lighting shall be set to minimise night-time glare.	✓		



	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Environmental Checklist</b>				
<b>Waste Management</b>				
<b>Construction Waste Management</b>				
▪ Relevant licence / permits for disposal of construction waste or excavated materials available for inspection.	√			
▪ Excavated material to be generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.	√			
▪ Mud and debris should be removed from waterworks access roads and associated drainage systems.	√			
▪ Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	√			
▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	√			
▪ Prior to disposal of C&D waste, recyclable materials should be salvaged for reuse (such as wood and metal) and inert waste utilised as public fill to minimise the quantity of waste to be disposed of to landfill.	√			
▪ In order to monitor the disposal of C&D material and solid wastes at public filling areas and landfills, and to control fly-tipping, a trip-ticket system should be included as one of the contractual requirements.	√			
▪ Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.	√			
<b>Chemical Waste Management</b>				
▪ It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	√			
▪ After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	√			
▪ Spent chemicals should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	√			
▪ Chemical wastes should be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facility.	√			
▪ Chemical wastes including waste oil should be stored properly in designated areas, e.g. chemical waste storage area.	√			
▪ The designated chemical waste storage area should only be used for storing chemical wastes.	√			
▪ The set-up of chemical waste storage area should				
▪ Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition.	√			
▪ Be enclosed on at least 3 sides and securely closed.	√			
▪ Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	√			
▪ Have adequate ventilation.	√			
▪ Be covered to prevent rainfall entering (water collected within the bund must be tested and disposal as chemical waste if necessary).	√			
▪ Be arranged so that incompatible materials are adequately separated.	√			



Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
Warning panels should be displayed at the waste storage area.	√			
Waste storage area should be cleaned and maintained regularly.	√			
Chemical waste should be transported by a registered chemical waste collector to a facility licensed to receive chemical waste.	√			
All generators, fuel and oil storage should be within bundle areas.	√			
Oil leakage from machinery, vehicle and plant should be prevented.	√			
In the event of chemical waste / dangerous goods / chemicals spillage or leakage, the procedures as outlined in the Spillage Response Plan should be followed.	√			
The dangerous goods / chemical spillage or leakage procedures (including equipments) should be in place.	√			
<b>Good Site Practices</b>				
Nomination of approved personnel, such as site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	√			
Training of site personnel in proper waste management and chemical handling procedures should be provided.	√			
Good site practices should be adopted to clean the rubbish and litter on a regular basis so as to prevent the rubbish and litter from dropping into the nearby environment.	√			
Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	√			
The Environmental Permit should be displayed conspicuously on site.	√			
Construction noise permits should be posted at site entrance or available for site inspection.	√			
Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	√			
Chemical storage area provided with lock and located on sealed areas.	√			
All chemicals should be placed at the banded area with adequate band capacity (>110% of largest tank).	√			
Any unused chemicals or those with remaining functional capacity should be recycled.	√			
Regular cleaning and maintenance programme for waste storage area, drainage systems, silt traps, sumps and oil interceptors.	√			
To encourage collection of aluminium cans by individual collectors.	√			
Separate labelled bins should be provided to segregate this waste from other general refuse generated by the workforce.	√			
A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	√			
A collection area should be provided where waste can be stored and loaded prior to removal from site. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. If an open area is unavoidable for the storage or loading/unloading of wastes, then the area should be banded and all the polluted surface run-off collected within this area should be diverted into wastewater treatment system.	√			



**Summary of the Weekly Site Inspection:**

Item	Details of defective works or observations	Proposed Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Target Completion Date
---	---	---	---	---	---

**Remark**

No defective work or observation was recorded during the weekly site inspection.

Name	Title	Signature	Date
Linda Law	Senior Environmental Officer		08 May 2014



CEDD Contract No.: CV/2013/06

Handling of Surplus Public Fill (2014-2016) - Tuen Mun Area 38 Fill Bank

Inspection Date : 15/5/14

Time : 10:30

Weather : Sunny / Fine / Cloudy / Overcast / Drizzle / Rain / Storm / Hazy

Wind : Calm / Light / Breeze / Strong

Temperature : 27°C

Humidity : High / Moderate / Low

Inspected by	CEDD	Contractor / Sub-Contractor	ET
Signature:			
Name:	LEE KI LING	Felix Chan	Mark Jui 'Man'
Title	100/p2	Surveyor	E.T

Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Fugitive Dust Emission</b>				
▪ Dust control / mitigation measures shall be provided to prevent dust nuisance.	√			
▪ Water sprays shall be provided and used to dampen materials.	√			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	√			
▪ Any vehicle with open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards. Material having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.	√			
▪ Unpaved areas should be watered regularly to avoid dust generation.	√			
▪ The designated site main haul road shall be paved or regular watering.	√			
▪ The haul road inside the site and public road around the site entrance should be kept clean and free from dust.	√			
▪ Wheel washing facilities including high-pressure water jet shall be provided at the entrance of work site.	√			
▪ Every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving the fill bank.	√			
▪ The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	√			
▪ Vehicle and equipment should be switched off while not in use.	√			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	√			
▪ Open burning should be prohibited.	√			
<b>Noise Impact</b>				
▪ The approved method of working, equipment and sound-reducing measures (e.g. use of silenced type of equipment, etc.) shall be adapted.	√			
▪ The constructions works should be scheduled to minimize noise nuisance.	√			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	√			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	√			
▪ Air compressors and hand held breakers should have noise labels.	√			
▪ Compressors and generators should operate with door closed.	√			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	√			
▪ Noisy equipment and mobile plant shall always be site away from NSRs.	√			



Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Water Quality</b>				
Drainage system and the sand / silt removal facilities should be adequate and well maintained to prevent flooding and overflow, especially after rain storms.	√			
The storm water intercepting system shall be effective to collect of runoff and remove suspended solids before discharge.	√			
Unnecessary water retained in receptacles and standing water should be avoided to prevent mosquito breeding.	√			
The material shall be properly covered to prevent washed away especially before rainstorm.	√			
The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	√			
Final slope surfaces, especially those facing to the north of the site shall be treated by compaction, followed by hydroseeding, vegetation planting or sealing with shotconcrete, latex, vinyl, bitumen, or other suitable surface stabilizer approved by CEDD.	√			
Existing and newly constructed Catchpits, sand and silt removal facilities and intercepting channels shall be maintained, and the deposited silt and grit shall be removed weekly and on a need basis especially at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	√			
A wheel washing bay shall be provided at the site exit and wash-water shall have sand and silt settled out or removed before being discharged into storm drains.	√			
The section of construction road between wheel washing bay and the public road shall be paved with concrete, bituminous materials or hardcore to reduce vehicle tracking of soil and to prevent silt run-off from entering public road drains.	√			
Sewage from toilets shall be discharged in to a foul sewer, or chemical toilets shall be provided.	√			
The chemical toilets (if use) shall be provided by a licensed contractor, who will be responsible for disposal and maintenance of these facilities.	√			
Tipping halls enclosed with top and 3-side to prevent spillage of material into marine water.	√			
The barges shall be in right size such that adequate clearance is maintained between the vessels and the seabed at all states of the tide to ensure the undue turbidity is not generated by turbulence from vessel movement or propeller wash.	√			
All vessels used for transportation of fill material shall have tight fitting seals to their bottom openings to prevent leakage of material during transport.	√			
Barges shall not be filled to a level which may cause the overflow of material during loading or transportation. Barge effluents shall be properly collected and treated before disposal.	√			
Adequate environmental control measures shall be provided to prevent / avoid dropping of fill material into the sea during the transfer.	√			
The work activities shall not cause any visible foam, oil, grease, scum, litter or other objectionable matters to be present on the water in the vicinity of the barging facilities.	√			
A waste collection vessel shall be deployed to remove floating debris.	√			
<b>Landscape and Visual</b>				
The maximum stockpiling height at the fill bank shall be limited to a maximum of +40mPD.	√			
Surface of outer slopes of the Fill Bank shall preferably be hydroseeded.	√			
Stockpile of public fill shall be removed in a sequence to allow the outer hydroseeded to be removed later than other portions as far as practicable.	√			
Casuarina equisetifolia were planted as buffer tree along the northern perimeter of the Site. The height of Casuarina equisetifolia was maintained at least 3m above soil level.	√			
Lighting shall be set to minimise night-time glare.	√			



Implementation Stages*	Implementation Stages*		Remark
	Yes	No	
<b>Environmental Checklist</b>			
<b>Waste Management</b>			
<b>Construction Waste Management</b>			
Relevant licence / permits for disposal of construction waste or excavated materials available for inspection.	√		
Excavated material to be generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.	√		
Mud and debris should be removed from waterworks access roads and associated drainage systems.	√		
Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	√		
Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	√		
Prior to disposal of C&D waste, recyclable materials should be salvaged for reuse (such as wood and metal) and inert waste utilised as public fill to minimise the quantity of waste to be disposed of to landfill.	√		
In order to monitor the disposal of C&D material and solid wastes at public filling areas and landfills, and to control fly-tipping, a trip-ticket system should be included as one of the contractual requirements.	√		
Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.	√		
<b>Chemical Waste Management</b>			
It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	√		
After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	√		
Spent chemicals should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	√		
Chemical wastes should be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facility.	√		
Chemical wastes including waste oil should be stored properly in designated areas, e.g. chemical waste storage area.	√		
The designated chemical waste storage area should only be used for storing chemical wastes.	√		
The set-up of chemical waste storage area should			
Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition.	√		
Be enclosed on at least 3 sides and securely closed.	√		
Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	√		
Have adequate ventilation.	√		
Be covered to prevent rainfall entering (water collected within the bund must be tested and disposal as chemical waste if necessary).	√		
Be arranged so that incompatible materials are adequately separated.	√		



	Implementation Stages*			Remark
	Yes	No	N/A	
<ul style="list-style-type: none"> <li>▪ Warning panels should be displayed at the waste storage area.</li> <li>▪ Waste storage area should be cleaned and maintained regularly.</li> <li>▪ Chemical waste should be transported by a registered chemical waste collector to a facility licensed to receive chemical waste.</li> <li>▪ All generators, fuel and oil storage should be within bundle areas.</li> <li>▪ Oil leakage from machinery, vehicle and plant should be prevented.</li> <li>▪ In the event of chemical waste / dangerous goods / chemicals spillage or leakage, the procedures as outlined in the Spillage Response Plan should be followed.</li> <li>▪ The dangerous goods / chemical spillage or leakage procedures (including equipments) should be in place.</li> </ul>	√			
<b>Good Site Practices</b>				
<ul style="list-style-type: none"> <li>▪ Nomination of approved personnel, such as site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.</li> <li>▪ Training of site personnel in proper waste management and chemical handling procedures should be provided.</li> <li>• Good site practices should be adopted to clean the rubbish and litter on a regular basis so as to prevent the rubbish and litter from dropping into the nearby environment.</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> <li>• The Environmental Permit should be displayed conspicuously on site.</li> <li>• Construction noise permits should be posted at site entrance or available for site inspection.</li> <li>▪ Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> <li>▪ Chemical storage area provided with lock and located on sealed areas.</li> <li>▪ All chemicals should be placed at the banded area with adequate band capacity (&gt;110% of largest tank).</li> <li>▪ Any unused chemicals or those with remaining functional capacity should be recycled.</li> <li>▪ Regular cleaning and maintenance programme for waste storage area, drainage systems, silt traps, sumps and oil interceptors.</li> <li>▪ To encourage collection of aluminium cans by individual collectors.</li> <li>▪ Separate labelled bins should be provided to segregate this waste from other general refuse generated by the workforce.</li> <li>▪ A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.</li> <li>▪ A collection area should be provided where waste can be stored and loaded prior to removal from site. An enclosed and covered area is preferred to reduce the occurrence of wind blown light material. If an open area is unavoidable for the storage or loading/unloading of wastes, then the area should be banded and all the polluted surface run-off collected within this area should be diverted into wastewater treatment system.</li> </ul>	√			



**Summary of the Weekly Site Inspection:**

Item	Details of defective works or observations	Proposed Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Target Completion Date
--		--	--	--	--

**Remark**

No defective work or observation was recorded during the weekly site inspection.

Name	Title	Signature	Date
Linda Law	Senior Environmental Officer		15 May 2014









CEDD Contract No.: CV/2013/06

Handling of Surplus Public Fill(2014-2016) - Tuen Mun Area 38 Fill Bank

Inspection Date : 22/5/14  
 Time : 14:15  
 Weather : Sunny / Fine / Cloudy / Overcast / Drizzle / Rain / Storm / Hazy  
 Wind : Calm / Light / Breeze / Strong  
 Temperature : 27°C  
 Humidity : High / Moderate / Low

Inspected by	CEDD	Contractor / Sub-Contractor	ET
Signature:			
Name:	Eric K. Ling	Eric K. Ling	
Title	100/P3	100/P3	ET



	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Fugitive Dust Emission</b>				
▪ Dust control / mitigation measures shall be provided to prevent dust nuisance.		✓		Item 1
▪ Water sprays shall be provided and used to dampen materials.	✓			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	✓			
▪ Any vehicle with open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards. Material having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.	✓			
▪ Unpaved areas should be watered regularly to avoid dust generation.	✓			
▪ The designated site main haul road shall be paved or regular watering.	✓			
▪ The haul road inside the site and public road around the site entrance should be kept clean and free from dust.	✓			
▪ Wheel washing facilities including high-pressure water jet shall be provided at the entrance of work site.	✓			
▪ Every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving the fill bank.	✓			
▪ The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	✓			
▪ Vehicle and equipment should be switched off while not in use.	✓			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	✓			
▪ Open burning should be prohibited.	✓			
<b>Noise Impact</b>				
▪ The approved method of working, equipment and sound-reducing measures (e.g. use of silenced type of equipment, etc.) shall be adapted.	✓			
▪ The constructions works should be scheduled to minimize noise nuisance.	✓			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	✓			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	✓			
▪ Air compressors and hand held breakers should have noise labels.	✓			
▪ Compressors and generators should operate with door closed.	✓			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	✓			
▪ Noisy equipment and mobile plant shall always be site away from NSRs.	✓			

	Implementation Stages*		Remark
	Yes	No	
<b>Water Quality</b>			
Drainage system and the sand / silt removal facilities should be adequate and well maintained to prevent flooding and overflow, especially after rain storms.	√		
The storm water intercepting system shall be effective to collect of runoff and remove suspended solids before discharge.	√		
Unnecessary water retained in receptacles and standing water should be avoided to prevent mosquito breeding.		√	Item 2
The material shall be properly covered to prevent washed away especially before rainstorm.	√		
The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	√		
Final slope surfaces, especially those facing to the north of the site shall be treated by compaction, followed by hydroseeding, vegetation planting or sealing with shotconcrete, latex, vinyl, bitumen, or other suitable surface stabilizer approved by CEDD.	√		
Existing and newly constructed Catchpits, sand and silt removal facilities and intercepting channels shall be maintained, and the deposited silt and grit shall be removed weekly and on a need basis especially at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	√		
A wheel washing bay shall be provided at the site exit and wash-water shall have sand and silt settled out or removed before being discharged into storm drains.	√		
The section of construction road between wheel washing bay and the public road shall be paved with concrete, bituminous materials or hardcores to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.	√		
Sewage from toilets shall be discharged in to a foul sewer, or chemical toilets shall be provided.	√		
The chemical toilets (if use) shall be provided by a licensed contractor, who will be responsible for disposal and maintenance of these facilities.	√		
Tipping halls enclosed with top and 3-side to prevent spillage of material into marine water.		√	Item 1
The barges shall be in right size such that adequate clearance is maintained between the vessels and the seabed at all states of the tide to ensure the undue turbidity is not generated by turbulence from vessel movement or propeller wash.	√		
All vessels used for transportation of fill material shall have tight fitting seals to their bottom openings to prevent leakage of material during transport.	√		
Barges shall not be filled to a level which may cause the overflow of material during loading or transportation. Barge effluents shall be properly collected and treated before disposal.	√		
Adequate environmental control measures shall be provided to prevent / avoid dropping of fill material into the sea during the transfer.	√		
The work activities shall not cause any visible foam, oil, grease, scum, litter or other objectionable matters to be present on the water in the vicinity of the barging facilities.	√		
A waste collection vessel shall be deployed to remove floating debris.	√		
<b>Landscape and Visual</b>			
The maximum stockpiling height at the fill bank shall be limited to a maximum of +40mPD.	√		
Surface of outer slopes of the Fill Bank shall preferably be hydroseeded.	√		
Stockpile of public fill shall be removed in a sequence to allow the outer hydroseeded to be removed later than other portions as far as practicable.	√		
Casuarina equisetifolia were planted as buffer tree along the northern perimeter of the Site. The height of Casuarina equisetifolia was maintained at least 3m above soil level.	√		
Lighting shall be set to minimise night-time glare.	√		



Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Waste Management</b>				
<b>Construction Waste Management</b>				
<ul style="list-style-type: none"> <li>▪ Relevant licence / permits for disposal of construction waste or excavated materials available for inspection.</li> <li>▪ Excavated material to be generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.</li> <li>▪ Mud and debris should be removed from waterworks access roads and associated drainage systems.</li> <li>▪ Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.</li> <li>▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>▪ Prior to disposal of C&amp;D waste, recyclable materials should be salvaged for reuse (such as wood and metal) and inert waste utilised as public fill to minimise the quantity of waste to be disposed of to landfill.</li> <li>▪ In order to monitor the disposal of C&amp;D material and solid wastes at public filling areas and landfills, and to control fly-tipping, a trip-ticket system should be included as one of the contractual requirements.</li> <li>▪ Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.</li> </ul>	√			
<b>Chemical Waste Management</b>				
<ul style="list-style-type: none"> <li>▪ It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</li> <li>▪ After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.</li> <li>▪ Spent chemicals should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.</li> <li>▪ Chemical wastes should be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facility.</li> <li>▪ Chemical wastes including waste oil should be stored properly in designated areas, e.g. chemical waste storage area.</li> <li>▪ The designated chemical waste storage area should only be used for storing chemical wastes.</li> <li>▪ The set-up of chemical waste storage area should               <ul style="list-style-type: none"> <li>▪ Be suitable for the substances they are holding, resistant to corrosion, maintained in a good condition.</li> <li>▪ Be enclosed on at least 3 sides and securely closed.</li> <li>▪ Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.</li> <li>▪ Have adequate ventilation.</li> <li>▪ Be covered to prevent rainfall entering (water collected within the bund must be tested and disposal as chemical waste if necessary).</li> <li>▪ Be arranged so that incompatible materials are adequately separated.</li> </ul> </li> </ul>	√			




	Implementation Stages*		Remark
	Yes	No / N/A	
▪ Warning panels should be displayed at the waste storage area.	✓		
▪ Waste storage area should be cleaned and maintained regularly.	✓		
▪ Chemical waste should be transported by a registered chemical waste collector to a facility licensed to receive chemical waste.	✓		
▪ All generators, fuel and oil storage should be within bundle areas.	✓		
▪ Oil leakage from machinery, vehicle and plant should be prevented.	✓		
▪ In the event of chemical waste / dangerous goods / chemicals spillage or leakage, the procedures as outlined in the Spillage Response Plan should be followed.	✓		
▪ The dangerous goods / chemical spillage or leakage procedures (including equipments) should be in place.	✓		
<b>Good Site Practices</b>			
▪ Nomination of approved personnel, such as site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	✓		
▪ Training of site personnel in proper waste management and chemical handling procedures should be provided.	✓		
• Good site practices should be adopted to clean the rubbish and litter on a regular basis so as to prevent the rubbish and litter from dropping into the nearby environment.	✓		
• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	✓		
• The Environmental Permit should be displayed conspicuously on site.	✓		
• Construction noise permits should be posted at site entrance or available for site inspection.	✓		
▪ Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	✓		
▪ Chemical storage area provided with lock and located on sealed areas.	✓		
▪ All chemicals should be placed at the banded area with adequate band capacity (>110% of largest tank).	✓		
▪ Any unused chemicals or those with remaining functional capacity should be recycled.	✓		
▪ Regular cleaning and maintenance programme for waste storage area, drainage systems, silt traps, sumps and oil interceptors.	✓		
▪ To encourage collection of aluminium cans by individual collectors.	✓		
▪ Separate labelled bins should be provided to segregate this waste from other general refuse generated by the workforce.	✓		
▪ A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	✓		
▪ A collection area should be provided where waste can be stored and loaded prior to removal from site. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. If an open area is unavoidable for the storage or loading/unloading of wastes, then the area should be banded and all the polluted surface run-off collected within this area should be diverted into wastewater treatment system.	✓		

**Summary of the Weekly Site Inspection:**

Item	Details of defective works or observations	Proposed Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Target Completion Date
1	The enclosure of tipping hall No.2 was damaged.	To repair the damaged part of tipping hall properly.	140522_001	Yes	29/05/14
2	Stagnant water was found accumulated inside the drip tray for a generator at work shop.	To drain off the stagnant water or apply pesticide to avoid mosquito breeding.	140522_002	Yes	29/05/14

Remark

--

Name	Title	Signature	Date
Linda Law	Senior Environmental Officer		22 May 2014

Photos

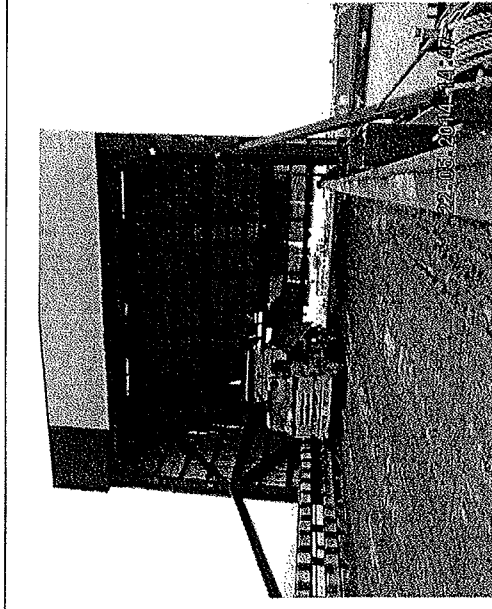





Photo 140522\_001 (Tipping hall No.2)



Photo 140522\_002 (Work shop)



Inspection Date : 29/5/14  
 Time : 10:00  
 Weather : Sunny / Fine / Cloudy / Overcast / Drizzle / Rain / Storm / Hazy  
 Wind : Calm / Light / Breeze / Strong  
 Temperature : 31°C  
 Humidity : High / Moderate / Low

Inspected by	CEDD	Contractor / Sub-Contractor	ET
Signature:			
Name:	Wai K. King	Mark Hei Wan	Mark Hei Wan
Title	LOA/PT	EO	E.T





Implementation Stages*		Remark
<b>Fugitive Dust Emission</b>		
√		Dust control / mitigation measures shall be provided to prevent dust nuisance.
√		Water sprays shall be provided and used to dampen materials.
√		All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.
√		Any vehicle with open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards. Material having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.
√		Unpaved areas should be watered regularly to avoid dust generation.
√		The designated site main haul road shall be paved or regular watering.
√		The haul road inside the site and public road around the site entrance should be kept clean and free from dust.
√		Wheel washing facilities including high-pressure water jet shall be provided at the entrance of work site.
√		Every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving the fill bank.
√		The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.
√		Vehicle and equipment should be switched off while not in use.
√		All plant and equipment should be well maintained e.g. without black smoke emission.
√		Open burning should be prohibited.
<b>Noise Impact</b>		
√		The approved method of working, equipment and sound-reducing measures (e.g. use of silenced type of equipment, etc.) shall be adapted.
√		The constructions works should be scheduled to minimize noise nuisance.
√		Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.
√		Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.
√		Air compressors and hand held breakers should have noise labels.
√		Compressors and generators should operate with door closed.
√		Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.
√		Noisy equipment and mobile plant shall always be site away from NSRs.



Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Water Quality</b>				
▪ Drainage system and the sand / silt removal facilities should be adequate and well maintained to prevent flooding and overflow, especially after rain storms.	√			
▪ The storm water intercepting system shall be effective to collect of runoff and remove suspended solids before discharge.	√			
▪ Unnecessary water retained in receptacles and standing water should be avoided to prevent mosquito breeding.	√			
▪ The material shall be properly covered to prevent washed away especially before rainstorm.	√			
▪ The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.	√			
▪ Final slope surfaces, especially those facing to the north of the site shall be treated by compaction, followed by hydroseeding, vegetation planting or sealing with shotconcrete, latex, vinyl, bitumen, or other suitable surface stabilizer approved by CEDD.	√			
▪ Existing and newly constructed Catchpits, sand and silt removal facilities and intercepting channels shall be maintained, and the deposited silt and grit shall be removed weekly and on a need basis especially at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	√			
▪ A wheel washing bay shall be provided at the site exit and wash-water shall have sand and silt settled out or removed before being discharged into storm drains.	√			
▪ The section of construction road between wheel washing bay and the public road shall be paved with concrete, bituminous materials or hardcores to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.	√			
▪ Sewage from toilets shall be discharged in to a foul sewer, or chemical toilets shall be provided.	√			
▪ The chemical toilets (if use) shall be provided by a licensed contractor, who will be responsible for disposal and maintenance of these facilities.	√			
▪ Tipping hails enclosed with top and 3-side to prevent spillage of material into marine water.	√		Item 1	
▪ The barges shall be in right size such that adequate clearance is maintained between the vessels and the seabed at all states of the tide to ensure the undue turbidity is not generated by turbulence from vessel movement or propeller wash.	√			
▪ All vessels used for transportation of fill material shall have tight fitting seals to their bottom openings to prevent leakage of material during transport.	√			
▪ Barges shall not be filled to a level which may cause the overflow of material during loading or transportation. Barge effluents shall be properly collected and treated before disposal.	√			
▪ Adequate environmental control measures shall be provided / avoid dropping of fill material into the sea during the transfer.	√			
▪ The work activities shall not cause any visible foam, oil, grease, scum, litter or other objectionable matters to be present on the water in the vicinity of the barging facilities.	√			
▪ A waste collection vessel shall be deployed to remove floating debris.	√			
<b>Landscape and Visual</b>				
▪ The maximum stockpiling height at the fill bank shall be limited to a maximum of +40mPD.	√			
▪ Surface of outer slopes of the Fill Bank shall preferably be hydroseeded.	√			
▪ Stockpile of public fill shall be removed in a sequence to allow the outer hydroseeded to be removed later than other portions as far as practicable.	√			
▪ Casuarina equisetifolia were planted as buffer tree along the northern perimeter of the Site. The height of Casuarina equisetifolia was maintained at least 3m above soil level.	√			
▪ Lighting shall be set to minimise night-time glare.	√			

Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
<b>Waste Management</b>				
<b>Construction Waste Management</b>				
▪ Relevant licence / permits for disposal of construction waste or excavated materials available for inspection.	√			
▪ Excavated material to be generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.	√			
▪ Mud and debris should be removed from waterworks access roads and associated drainage systems.	√			
▪ Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	√			
▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	√			
▪ Prior to disposal of C&D waste, recyclable materials should be salvaged for reuse (such as wood and metal) and inert waste utilised as public fill to minimise the quantity of waste to be disposed of to landfill.	√			
▪ In order to monitor the disposal of C&D material and solid wastes at public filling areas and landfills, and to control fly-tipping, a trip-ticket system should be included as one of the contractual requirements.	√			
▪ Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.	√			
<b>Chemical Waste Management</b>				
▪ It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	√			
▪ After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	√			
▪ Spent chemicals should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	√			
▪ Chemical wastes should be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facility.	√			
▪ Chemical wastes including waste oil should be stored properly in designated areas, e.g. chemical waste storage area.	√			
▪ The designated chemical waste storage area should only be used for storing chemical wastes.	√			
▪ The set-up of chemical waste storage area should				
▪ Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition.	√			
▪ Be enclosed on at least 3 sides and securely closed.	√			
▪ Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	√			
▪ Have adequate ventilation.	√			
▪ Be covered to prevent rainfall entering (water collected within the bund must be tested and disposal as chemical waste if necessary).	√			
▪ Be arranged so that incompatible materials are adequately separated.	√			




Environmental Checklist	Implementation Stages*			Remark
	Yes	No	N/A	
▪ Warning panels should be displayed at the waste storage area.	√			
▪ Waste storage area should be cleaned and maintained regularly.	√			
▪ Chemical waste should be transported by a registered chemical waste collector to a facility licensed to receive chemical waste.	√			
▪ All generators, fuel and oil storage should be within bundle areas.	√			
▪ Oil leakage from machinery, vehicle and plant should be prevented.	√			
▪ In the event of chemical waste / dangerous goods / chemicals spillage or leakage, the procedures as outlined in the Spillage Response Plan should be followed.	√			
▪ The dangerous goods / chemical spillage or leakage procedures (including equipments) should be in place.	√			
<b>Good Site Practices</b>				
▪ Nomination of approved personnel, such as site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	√			
▪ Training of site personnel in proper waste management and chemical handling procedures should be provided.	√			
• Good site practices should be adopted to clean the rubbish and litter on a regular basis so as to prevent the rubbish and litter from dropping into the nearby environment.	√			
• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	√			
• The Environmental Permit should be displayed conspicuously on site.	√			
• Construction noise permits should be posted at site entrance or available for site inspection.	√			
▪ Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	√			
▪ Chemical storage area provided with lock and located on sealed areas.	√			
▪ All chemicals should be placed at the banded area with adequate band capacity (>110% of largest tank).	√			
▪ Any unused chemicals or those with remaining functional capacity should be recycled.	√			
▪ Regular cleaning and maintenance programme for waste storage area, drainage systems, silt traps, sumps and oil interceptors.	√			
▪ To encourage collection of aluminium cans by individual collectors.	√			
▪ Separate labelled bins should be provided to segregate this waste from other general refuse generated by the workforce.	√			
▪ A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	√			
▪ A collection area should be provided where waste can be stored and loaded prior to removal from site. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. If an open area is unavoidable for the storage or loading/unloading of wastes, then the area should be banded and all the polluted surface run-off collected within this area should be diverted into wastewater treatment system.	√			

**Summary of the Weekly Site Inspection:**

Item	Details of defective works or observations	Proposed Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Target Completion Date
1	Follow up action to item 1 on 22/05/14, the enclosure of tipping hall No.2 was still found damaged.	To repair the damaged part of tipping hall properly.	140529_001	Yes	05/06/14
2	Follow up action to item 2 on 22/05/14, stagnant water accumulated inside the drip tray for a generator at work shop was cleared.	---	140529_002	No	---

Remark

--

Name	Title	Signature	Date
Linda Law	Senior Environmental Officer		29 May 2014

Photos


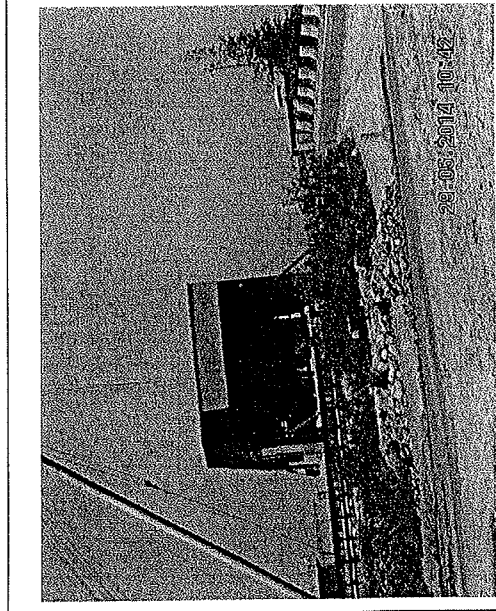


Photo 140529\_001 (Tipping hall No.2)



Photo 140522\_002 (Work shop)

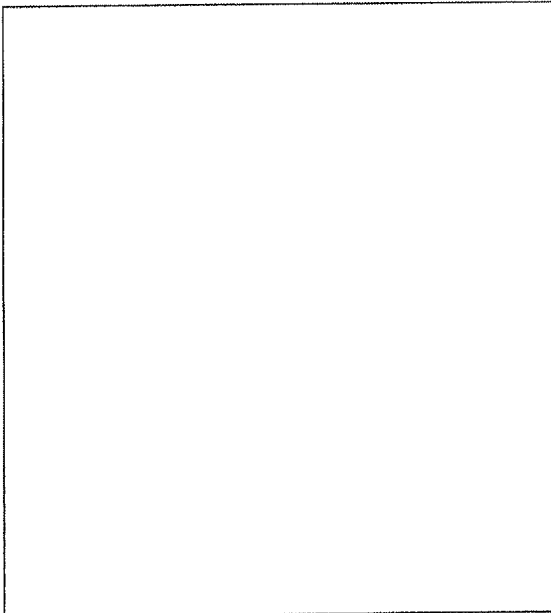

## **Appendix I**

### **Implementation Schedule of Mitigation Measures**



## Environmental Mitigation Implementation Schedule

	Location	Implementation Status		
		Implemented	Partially implemented	Not implemented
<b>Environmental Protection Measures</b>				
<b>Air Quality</b>				
<ul style="list-style-type: none"> <li>▪ Dust control / mitigation measures shall be provided to prevent dust nuisance.</li> <li>▪ Water sprays shall be provided and used to dampen materials.</li> <li>▪ All stockpile of aggregate or soil should be enclosed or covered and water applied in dry or windy condition.</li> <li>▪ Any vehicle with open load carrying area used for moving materials which has the potential to create dust shall have properly fitting side and tail boards. Material having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin.</li> <li>▪ Unpaved areas should be watered regularly to avoid dust generation.</li> <li>▪ The designated site main haul road shall be paved or regular watering.</li> <li>▪ The public road around the site entrance should be kept clean and free from dust.</li> <li>▪ Wheel washing facilities including high-pressure water jet shall be provided at the entrance of work site.</li> <li>▪ Every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving the fill bank.</li> <li>▪ The temporary slope surfaces shall be covered with impermeable sheet or sprayed with water.</li> <li>▪ Vehicle and equipment should be switched off while not in use.</li> <li>▪ All plant and equipment should be well maintained e.g. without black smoke emission.</li> <li>▪ Open burning should be prohibited.</li> </ul>				
<b>Noise Impact</b>				
<ul style="list-style-type: none"> <li>▪ The approved method of working, equipment and sound-reducing measures (e.g. use of silenced type of equipment, etc.) shall be adapted.</li> <li>▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.</li> <li>▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.</li> <li>▪ Air compressors and hand held breakers should have noise labels.</li> <li>▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.</li> <li>▪ Noisy equipment and mobile plant shall always be site away from NSRs.</li> </ul>				







	Location	Implementation Status			
		Implemented	Partially implemented	Not implemented	Not Applicable
<ul style="list-style-type: none"> <li>Excavated material to be generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Mud and debris should be removed from waterworks access roads and associated drainage systems.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Prior to disposal of C&amp;D waste, recyclable materials should be salvaged for reuse (such as wood and metal) and inert waste utilised as public fill to minimise the quantity of waste to be disposed of to landfill.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>In order to monitor the disposal of C&amp;D material and solid wastes at public filling areas and landfills, and to control fly-tipping, a trip-ticket system should be included as one of the contractual requirements.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.</li> </ul>	All areas	√			
<b>Chemical Waste Management</b>					
<ul style="list-style-type: none"> <li>It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Spent chemicals should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Chemical wastes should be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facility.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Chemical wastes including waste oil should be stored properly in designated areas, e.g. chemical waste storage area.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>The designated chemical waste storage area should only be used for storing chemical wastes.</li> </ul>	Waste Storage Area	√			
<b>The set-up of chemical waste storage area should</b>					
<ul style="list-style-type: none"> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Be enclosed on at least 3 sides and securely closed.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Have adequate ventilation.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposal as chemical waste if necessary).</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Be arranged so that incompatible materials are adequately separated.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Warning panels should be displayed at the waste storage area.</li> </ul>	Waste Storage Area	√			



Environmental Protection Measures		Location	Implementation Status		
			Implemented	Partially implemented	Not implemented
<ul style="list-style-type: none"> <li>Waste storage area should be cleaned and maintained regularly.</li> </ul>	Waste Storage Area	√			
<ul style="list-style-type: none"> <li>Chemical waste should be transported by a registered chemical waste collector to a facility licensed to receive chemical waste.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>All generators, fuel and oil storage should be within bundle areas.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Oil leakage from machinery, vehicle and plant should be prevented.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>In the event of chemical waste / dangerous goods / chemicals spillage or leakage, the procedures as outlined in the Spillage Response Plan should be followed.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>The dangerous goods / chemical spillage or leakage procedures (including equipments) should be in place.</li> </ul>	All areas	√			
<b>Good Site Practices</b>					
<ul style="list-style-type: none"> <li>Nomination of approved personnel, such as site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Training of site personnel in proper waste management and chemical handling procedures should be provided.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Good site practices should be adopted to clean the rubbish and litter on a regular basis so as to prevent the rubbish and litter from dropping into the nearby environment.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>The Environmental Permit should be displaced conspicuously on site.</li> </ul>	Site Entrance	√			
<ul style="list-style-type: none"> <li>Construction noise permits should be posted at site entrance or available for site inspection.</li> </ul>	Site Entrance				√
<ul style="list-style-type: none"> <li>Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Chemical storage area provided with lock and located on sealed areas.</li> </ul>	Chemical Storage Area	√			
<ul style="list-style-type: none"> <li>All chemicals should be placed at the banded area with adequate band capacity (&gt;110% of largest tank).</li> </ul>	Chemical Storage Area	√			
<ul style="list-style-type: none"> <li>Any unused chemicals or those with remaining functional capacity should be recycled.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Regular cleaning and maintenance programme for waste storage area, drainage systems, silt traps, sumps and oil interceptors.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>To encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to segregate this waste from other general refuse generated by the workforce.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>A collection area should be provided where waste can be stored and loaded prior to removal from site. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. If an open area is unavoidable for the storage or loading/unloading of wastes, then the area should be banded and all the polluted surface run-off collected within this area should be diverted into wastewater treatment system.</li> </ul>	All areas	√			
<ul style="list-style-type: none"> <li>Remove wastes in a timely manner.</li> </ul>	All areas	√			



**Appendix J**  
**Site General Layout plan**

- NOTES:
1. DIMENSIONS REFER TO HORIZONTAL DIMENSIONS UNLESS OTHERWISE SPECIFIED.
  2. ALL LEVELS REFER TO HONG KONG PRINCIPAL LEVEL (P.C.L.) UNLESS OTHERWISE SPECIFIED.
  3. ALL DIMENSIONS ARE IN METRES.

LEGEND:

- SITE BOUNDARY
- - - - - EXISTING HOUSING
- - - - - EXISTING GATE
- ⊗ BAY
- ⊗ BAY WASHING AREA
- ⊗ EXISTING RECEIVING POINT BY 4TH 3 WHEELS (P.S. 3)
- ⊗ PROPOSED CITY 4TH TOWER
- ⊗ PROPOSED CITY 4TH TOWER ON THE EXISTING POST



REV.	DATE	DESCRIPTION	BY	CHECKED	APPROVED
1	15/11/2016	ISSUED FOR PERMIT	...	...	...
2	15/11/2016	ISSUED FOR PERMIT	...	...	...
3	15/11/2016	ISSUED FOR PERMIT	...	...	...

DATE: 15/11/2016  
 CONTRACT NO.: CV/2013/06  
 PROJECT NO.:  
 CONTRACTOR:

HANDLING OF SURPLUS PUBLIC FILL (2014-2016)  
 TUN MUN AREA 38 FILL BANK - GENERAL LAYOUT


DRAWING NO.: FMT10068-16  
 SCALE: 1:2000  
 AS SHOWN

OFFICE: FILL MANAGEMENT DIVISION CIVIL ENGINEERING OFFICE  
 CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

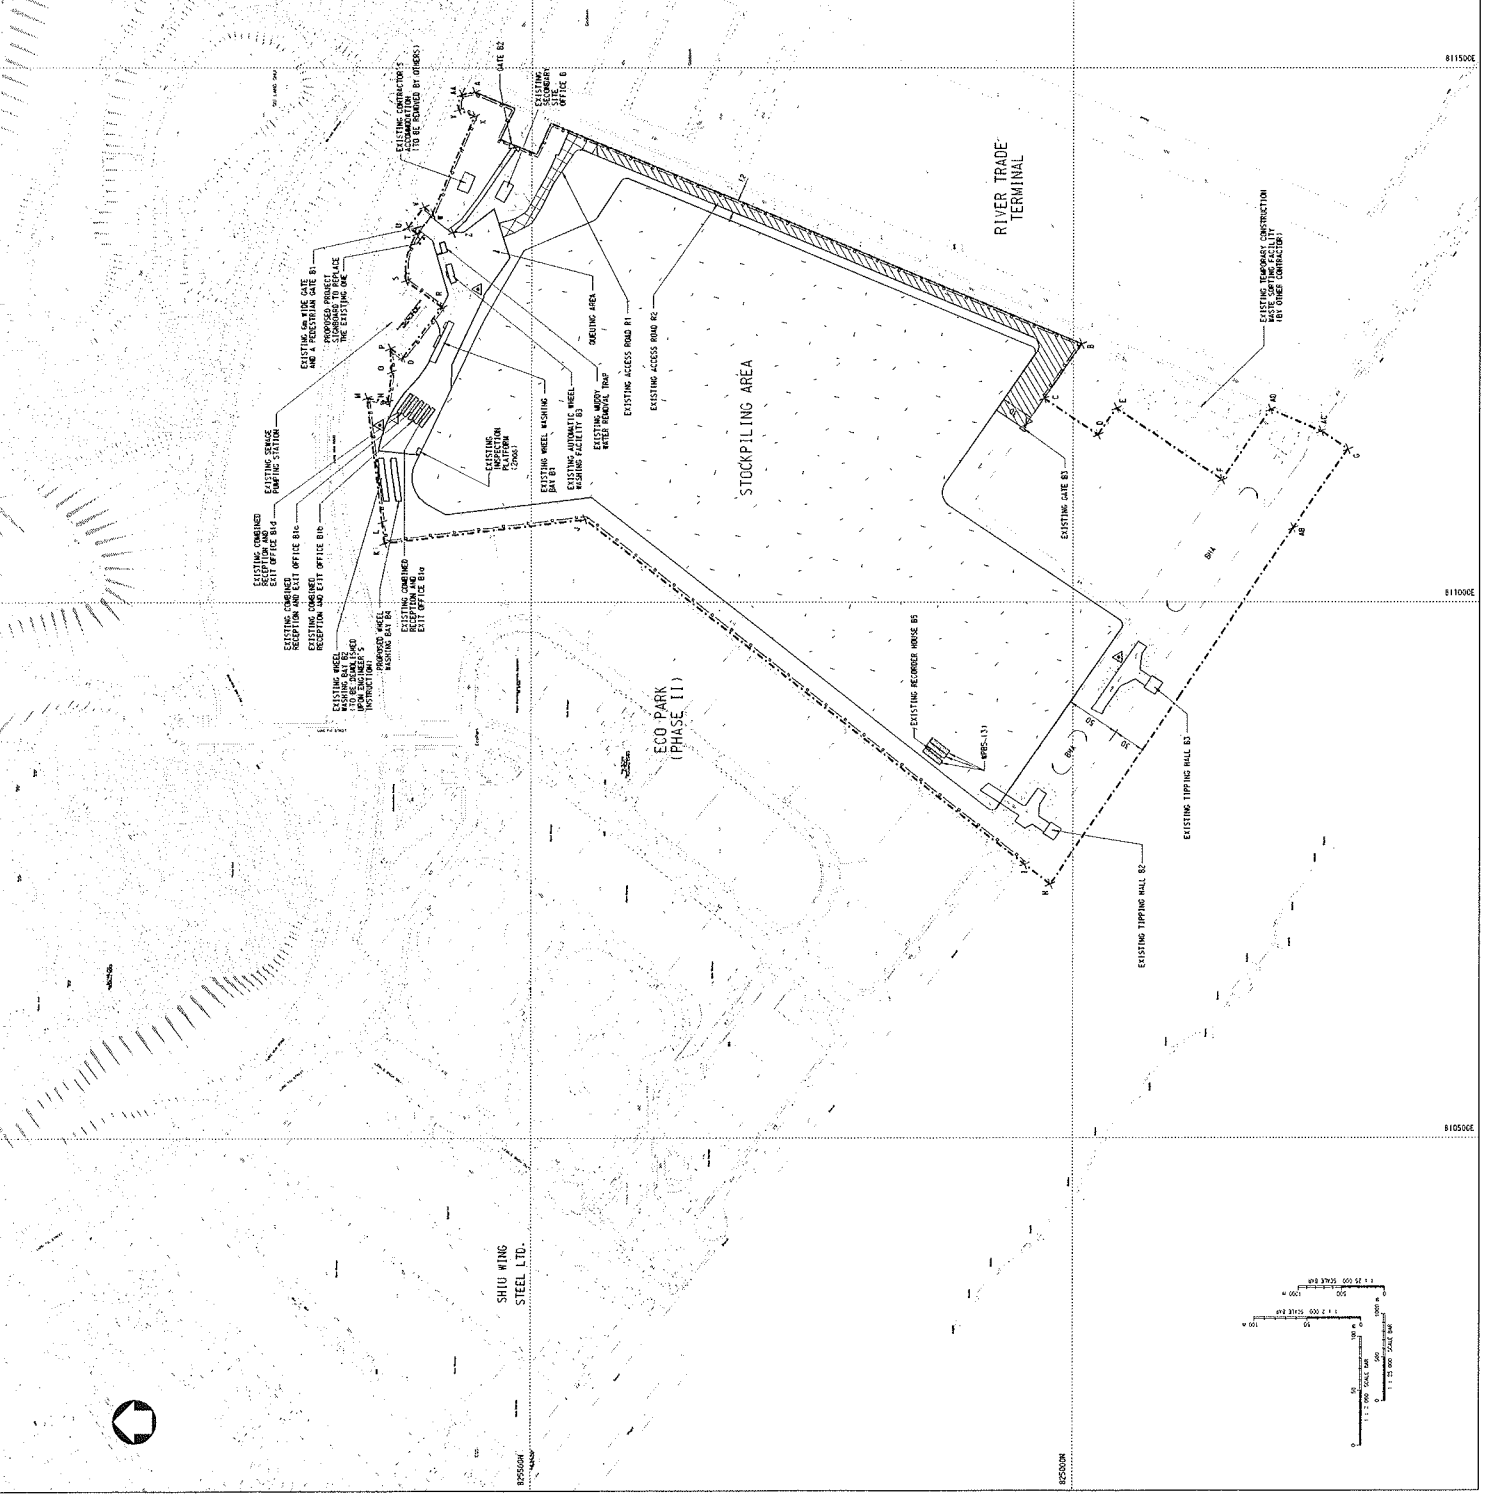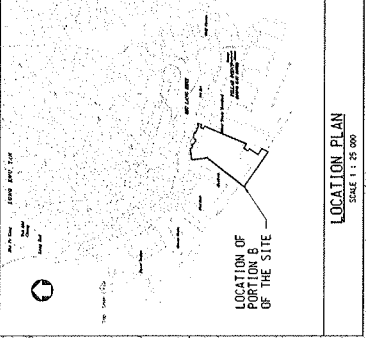

SETTING-OUT DETAILS

POINT	EASTING	NORTHING
A	811477.427	825931.893
B	811241.559	824992.231
C	811241.559	825007.337
D	811181.764	824992.231
E	811181.764	824962.326
F	811141.669	824961.853
G	811141.262	824944.271
H	810734.633	825001.002
I	810734.633	825044.511
J	810734.633	825051.660
K	810734.633	825051.660
L	810734.633	825051.660
M	811181.576	825031.111
N	811181.576	825031.111
O	811241.559	825027.314
P	811241.559	825029.194
Q	811241.559	825031.111
R	811241.559	825031.111
S	811241.559	825031.111
T	811241.559	825031.111
U	811241.559	825031.111
V	811241.559	825031.111
W	811241.559	825031.111
X	811241.559	825031.111
Y	811241.559	825031.111
Z	811241.559	825031.111
AA	811241.559	825031.111
AB	811241.559	825031.111
AC	811241.559	825031.111
AD	811241.559	825031.111



COPYRIGHT RESERVED

811500E

811000E

810500E

SHU HING STEEL LTD.



## Appendix K

### QA/QC Results of Laboratory Analysis



## QA/QC Results of Laboratory Analysis of Total Suspended Solids

Sampling Date	QC Sample Analysis	Sample Duplicate		Sample Spike	
	% Recovery *	Sample ID	% Error #	Sample ID	% Recovery @
03/05/14	97.0	FC1-S	0.0	FM2-M	104.0
	104.3	FM2-B	0.0	EM1-S	98.3
	107.8	EM1-M	0.0	EC2-B	96.2
08/05/14	99.0	FC1-S	8.0	FM2-M	92.2
	102.9	FM2-B	0.0	EM1-S	100.0
	95.0	EM1-M	8.0	EC2-B	93.8
10/05/14	106.0	FC1-S	7.4	FM2-M	104.3
	108.0	FM2-B	8.0	EM1-S	100.0
	95.5	EM1-M	0.0	EC2-B	91.8
13/05/14	97.2	FC1-S	8.0	FM2-M	92.2
	95.0	FM2-B	0.0	EM1-S	96.6
	95.0	EM1-M	7.4	EC2-B	95.5
15/05/14	105.0	FC1-S	0.0	FM2-M	100.0
	102.5	FM2-B	7.4	EM1-S	94.1
	94.9	EM1-M	0.0	EC2-B	96.7
17/05/14	105.7	FC1-S	0.0	FM2-M	109.4
	98.9	FM2-B	0.0	EM1-S	100.0
	100.0	EM1-M	5.7	EC2-B	100.0
20/05/14	106.3	FC1-S	6.9	FM2-M	98.4
	103.5	FM2-B	0.0	EM1-S	106.0
	102.7	EM1-M	0.0	EC2-B	97.1
22/05/14	106.0	FC1-S	9.5	FM2-M	104.4
	105.8	FM2-B	0.0	EM1-S	100.0
	92.6	EM1-M	8.0	EC2-B	95.1
24/05/14	103.5	FC1-S	0.0	FM2-M	101.4
	97.6	FM2-B	8.0	EM1-S	98.0
	93.8	EM1-M	0.0	EC2-B	93.2
27/05/14	93.1	FC1-S	6.5	FM2-M	95.2
	101.6	FM2-B	5.4	EM1-S	103.8
	94.9	EM1-M	5.4	EC2-B	100.0
29/05/14	92.1	FC1-S	6.9	FM2-M	98.4
	101.3	FM2-B	0.0	EM1-S	100.0
	99.6	EM1-M	5.7	EC2-B	92.2
31/05/14	99.0	FC1-S	6.9	FM2-M	101.5
	107.5	FM2-B	5.7	EM1-S	101.6
	94.0	EM1-M	5.7	EC2-B	91.2

Note: (\*) % Recovery of QC sample should be between 80% to 120%.  
(#) % Error of Sample Duplicate should be between -10% to 10%.  
(@) % Recovery of Sample Spike should be between 80% to 120%.



## **Appendix L**

### **Complaint Log**






## Complaint Log

Log Ref.	Location	Received Date	Details of Complaint	Investigation / Mitigation Action	Status
---	---	---	---	---	---



## Figures

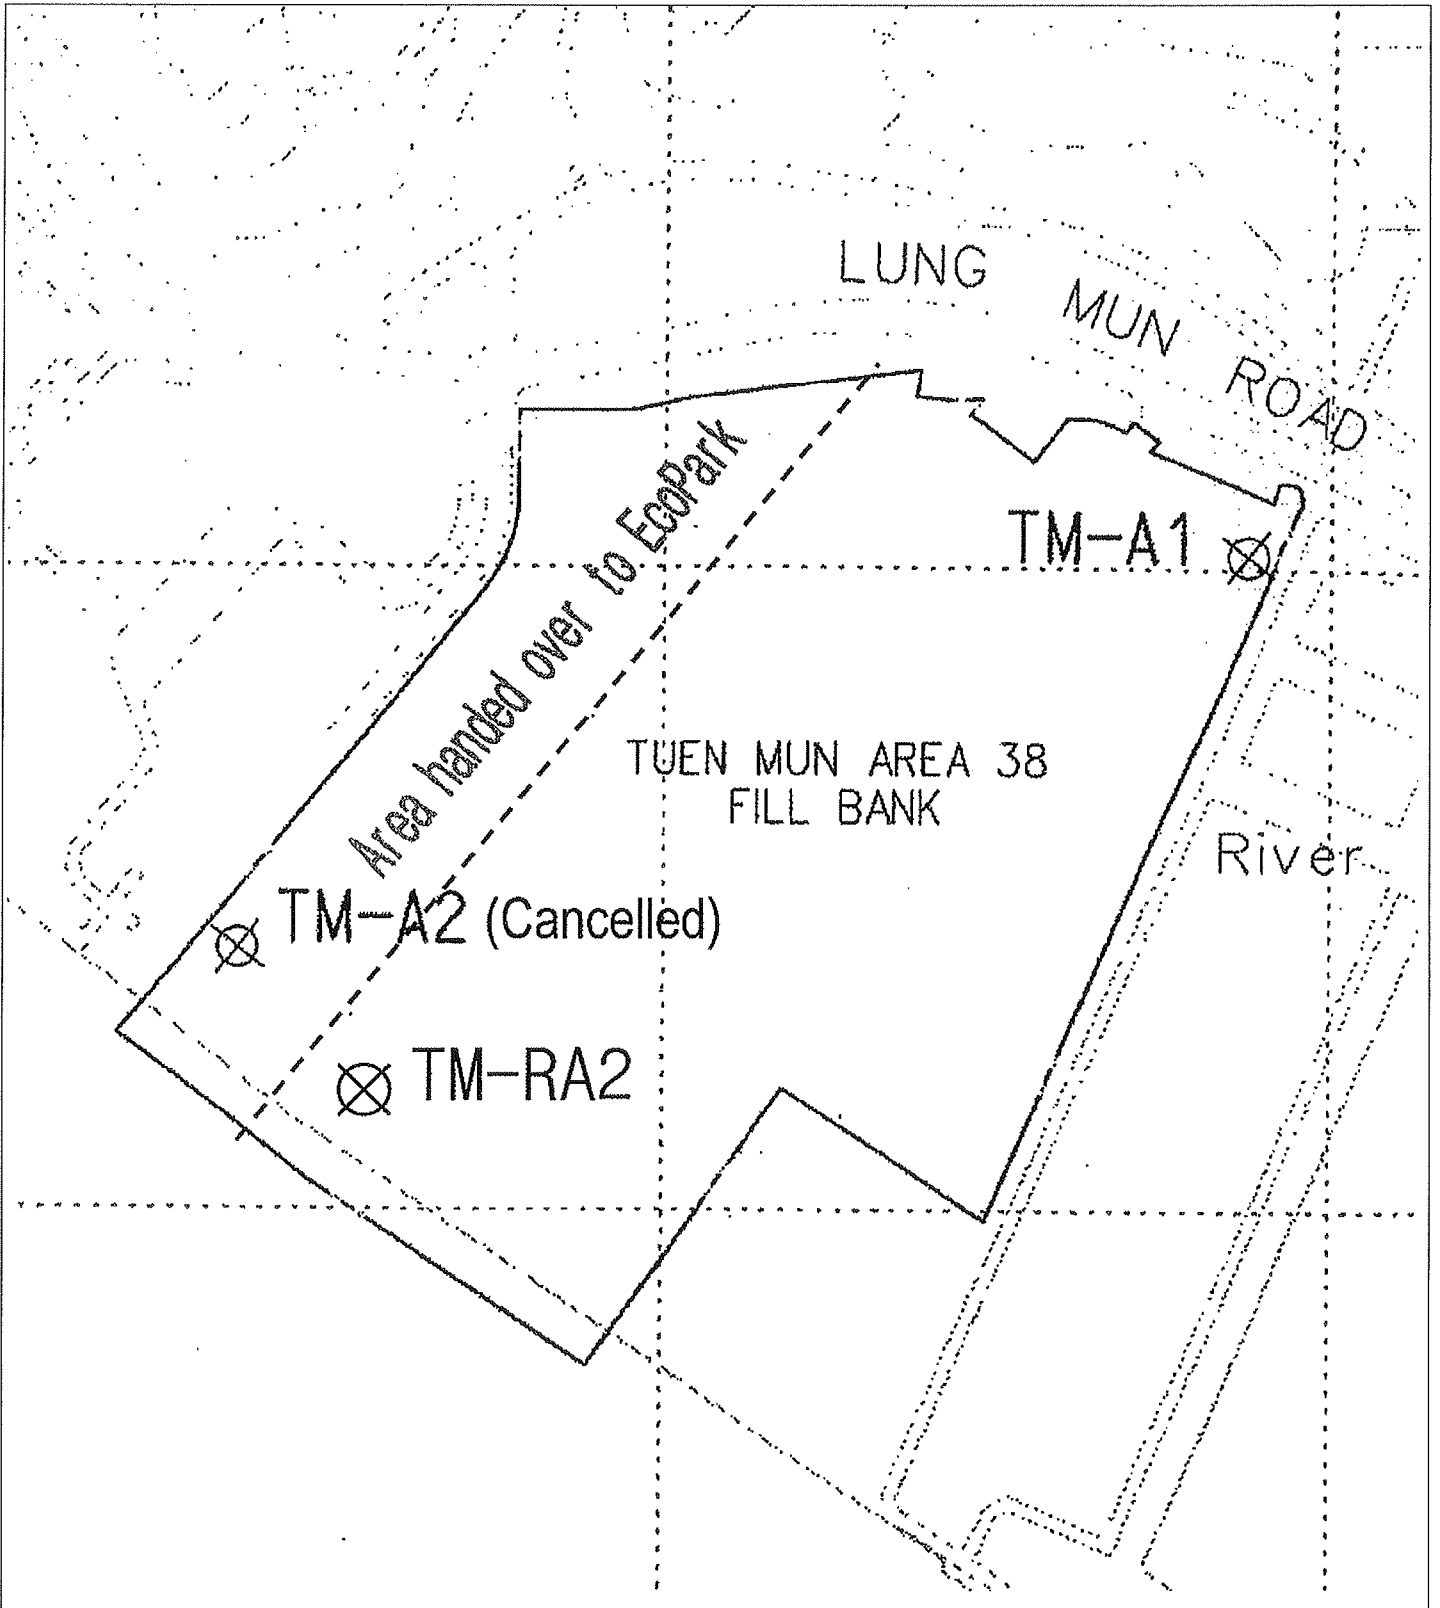


Contract No. CV/2013/06  
 Handling of Surplus Public Fill (2014-2016)

Figure 1  
 Locations of Air Quality Monitoring Stations –  
 Tuen Mun Area 38 Fill Bank



東業德勤測試顧問有限公司  
 ETS-TESTCONSULT LIMITED

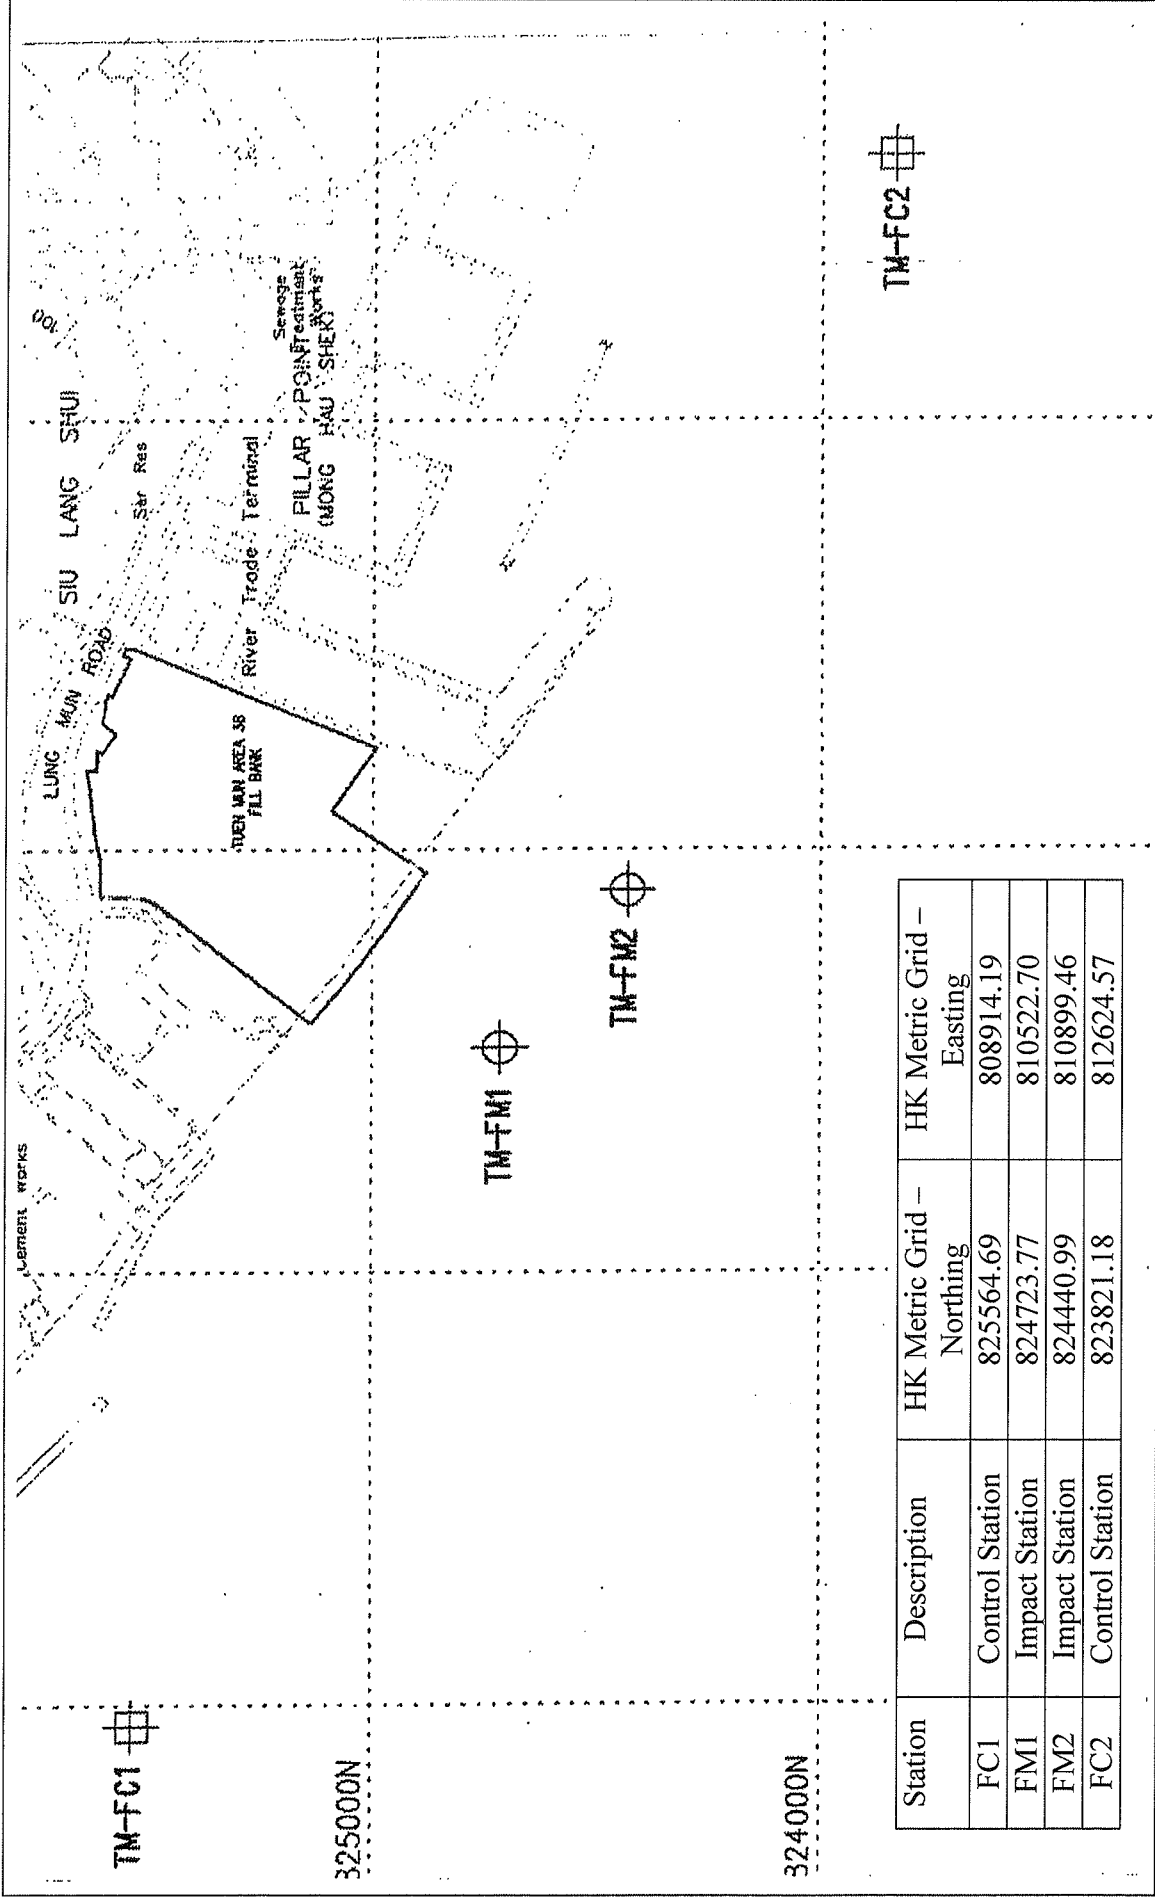


Station	Description	HK Metric Grid – Northing	HK Metric Grid – Easting
FC1	Control Station	825564.69	808914.19
FM1	Impact Station	824723.77	810522.70
FM2	Impact Station	824440.99	810899.46
FC2	Control Station	823821.18	812624.57

Contract No. CV/2013/06  
 Handling of Surplus Public Fill (2014-2016)



Figure 2  
 Locations of Water Quality Monitoring Station –  
 Tuen Mun Area 38 Fill Bank

東業德勤測試顧問有限公司  
 ETS-TESTCONSULT LIMITED

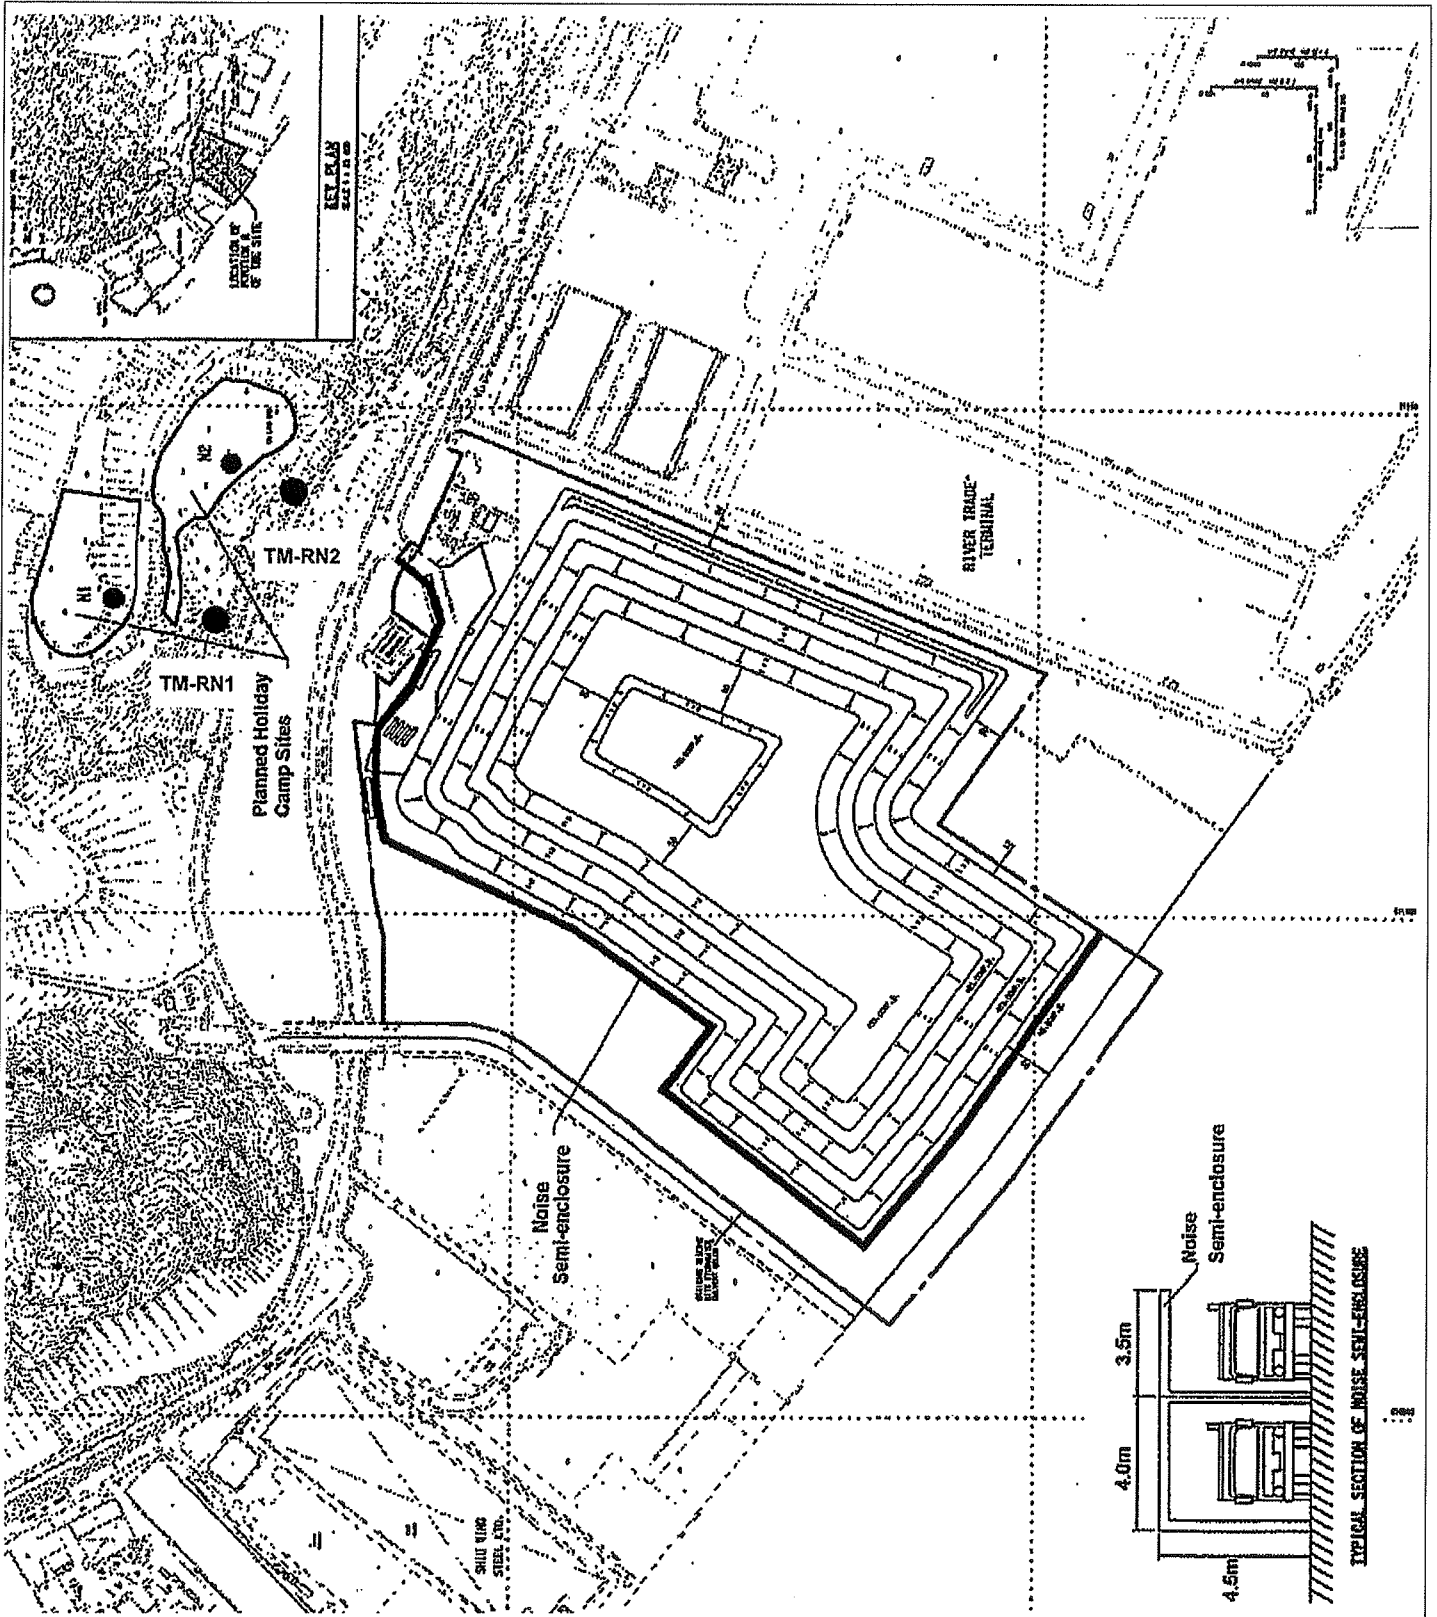

Contract No. CV/2013/06  
 Handling of Surplus Public Fill (2014-2016)

Figure 3  
 Locations of Noise Quality Monitoring Stations –  
 Tuen Mun Area 38 Fill Bank
