


# Sun Fook Kong – Bestwise Joint Venture

## Contract No. DC/2009/10 HATS Stage 2A – Upgrading Works at Stonecutters Island Sewage Treatment Works - Main Pumping Station, Sedimentation Tanks and Ancillary Facilities

Monthly Environmental  
Monitoring and Audit Report  
April 2021

(Version 1.0)

Certified By   
(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

Wellab accepts no responsibility for changes made to this report by third parties

**WELLAB LTD**  
Room 1714, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong  
Tel: (852) 2898 2083 Fax: (852) 2898 7076  
Email: [info@wellab.com.hk](mailto:info@wellab.com.hk)

CE/Harbour Area Treatment Scheme  
Drainage Services Department  
Sewage Services Branch  
Harbour Area Treatment Scheme Division  
5/F, Western Magistracy  
2A Pokfulam Road, Hong Kong

Attn: Mr. K K Kam

**Agreement No. CE 8/2009(EP) Harbour Area Treatment Scheme Stage 2A  
Independent Environmental Checker for Construction Phase – Investigation**

**Our Reference**  
EC/AFK/DC/bw/T261332/  
22.01/L-1494

**Contract No. DC/2009/10 – Upgrading Works at Stonecutters Island Sewage  
Treatment Works – Main Pumping Station, Sedimentation Tanks and Ancillary  
Facilities**

3/F International Trade  
Tower  
348 Kwun Tong Road  
Kowloon  
Hong Kong

**Condition 4.4 – Monthly EM&A Report for April 2021 (no. 121) Version 1.0**

T +852 2828 5757  
F +852 2827 1823  
mottmac.hk

11 May 2021

**By Post**

Dear Sir,

I refer to the captioned Monthly EM&A Report for April 2021 (version 1.0) submitted by ET on 10 May 2021 via email. In accordance with Condition 4.4 of Environmental Permit No. EP-322/2008/G, I hereby verify the captioned Monthly EM&A Report.

Yours faithfully  
for MOTT MACDONALD HONG KONG LIMITED



Ir Dr Anne F Kerr  
Independent Environmental Checker  
T +852 2828 5757  
anne.kerr@mottmac.com

c.c.  
Ove Arup & Partners HK Limited  
Sun Fook Kong – Bestwise Joint Venture  
Wellab Limited

Mr. Mark Ngan  
Mr. Keith Ho  
Dr. Priscilla Choy

Fax: 2370 4377  
By email  
By email

# TABLE OF CONTENTS

	Page
<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
Introduction .....	1
Environmental Monitoring Works .....	1
Environmental Licenses and Permits .....	2
Environmental Mitigation Implementation Schedule .....	2
Key Information in the Reporting Month .....	2
Summary of Complaints and Prosecutions .....	2
Future Key Issues .....	3
<b>1. INTRODUCTION .....</b>	<b>4</b>
Background .....	4
Project Organizations .....	4
Summary of EM&A Requirements .....	5
<b>2. AIR QUALITY .....</b>	<b>6</b>
Monitoring Requirements .....	6
Monitoring Locations .....	6
Monitoring Equipment .....	6
Monitoring Parameters, Frequency and Duration .....	6
Monitoring Methodology and QA/QC Procedure .....	6
Results and Observations .....	9
<b>3. NOISE.....</b>	<b>10</b>
Monitoring Requirements .....	10
Monitoring Locations .....	10
Monitoring Equipment .....	10
Monitoring Parameters, Frequency and Duration .....	10
Monitoring Methodology and QA/QC Procedures .....	11
Results and Observations .....	12
<b>4. ENVIRONMENTAL AUDIT .....</b>	<b>13</b>
Site Audits .....	13
Implementation Status of Environmental Mitigation Measures .....	13
Review of Environmental Monitoring Procedures .....	13
Status of Environmental Licensing and Permitting .....	13
Status of Waste Management .....	14
Implementation Status of Event Action Plans .....	14
Summary of Complaints and Prosecutions .....	14
<b>5. FUTURE KEY ISSUES .....</b>	<b>15</b>
Key Issues for the Coming Month .....	15
Monitoring Schedule for the Next Month .....	15
Construction Program for the Next Month .....	15
<b>6. CONCLUSIONS AND RECOMMENDATIONS .....</b>	<b>16</b>
Conclusions .....	16
Recommendations for next reporting month .....	16

## **LIST OF TABLES**

Table I	Summary Table for Non-compliance Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 2.4	Summary of 1-hour and 24-hour TSP Monitoring Result in Reporting Month
Table 3.1	Locations for Noise Monitoring Stations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Summary the Noise Monitoring Results in Reporting Month
Table 4.1	Observations of Site Audit
Table 4.2	Summary of Environmental Licence / Permit for DC/2009/10

## **LIST OF FIGURES**

Figure 1	General Location Plan of the Project and Locations of Air Quality and Noise Monitoring Stations
Figure 2	ET's Organization Chart

## **LIST OF APPENDICES**

A	Action and Limit Levels for Air Quality and Noise
B	Copies of Calibration Certificates
C	Environmental Monitoring Schedules
D	1-hour and 24-hour TSP Monitoring Results and Graphical Presentations
E	Noise Monitoring Results and Graphical Presentations
F	Summary of Exceedance
G	Site Audit Summary
H	Summary of Amount of Waste Generated
I	Event Action Plans
J	Environmental Mitigation Implementation Schedule (EMIS)
K	Complaint Log
L	Construction Programme

## ABBREVIATION AND ACRONYM

AL Levels	Action and Limit Levels
DSD	Drainage Services Department
E / ER	Engineer/Engineer's Representative
EIA	Environmental Impact Assessment
EM&A	Environmental Monitoring and Audit
EMIS	Environmental Mitigation Implementation Schedule
EP	Environmental Permit
EPD	Environmental Protection Department
ET	Environmental Team
HVS	High Volume Sampler
IEC	Independent Environmental Checker
RE	Resident Engineer
RH	Relative Humidity
QA/QC	Quality Assurance / Quality Control
SLM	Sound Level Meter
WMP	Waste Management Plan
SCISTW	Stonecutters Island Sewage Treatment Works
HATS Stage 2A	Harbour Area Treatment Scheme Stage 2A
SBJV	Sun Fook Kong - Bestwise Joint Venture

**EXECUTIVE SUMMARY****Introduction**

1. This is the 121<sup>st</sup> Monthly Environmental Monitoring and Audit (EM&A) Report prepared by Wellab Limited for DSD Contract No. DC/2009/10 “HATS Stage 2A – Upgrading Works at Stonecutters Island Treatment Works – Main Pumping Station, Sedimentation Tanks and Ancillary Facilities” (The Project) which documents the key information of EM&A and environmental monitoring works undertaken by other Contracts at the SCISTW under HATS Stage 2A with the same Environmental Permit (Permit No. EP-322/2008/G).
2. The site activities undertaken in the reporting month included:

MPS2

- Defects rectification (on-going)
- DOU3 upgrading works

CEPT

- Observation for south PST & SMDC (Stage 3 CEPT handover) in progress
- Defect rectification and inspection for FT6 in progress

**Environmental Monitoring Works**

3. The environmental monitoring works of the Project were conducted by the ETs for Contract DC/2009/10, at the SCISTW under HATS 2A with the same Environmental Permit. The monitoring results were checked and reviewed and the site audits were conducted once per week. The implementation of the Environmental Mitigation Measures, Event Action Plans and Environmental Complaint Handling Procedures were also checked.
4. Summary of the non-compliance of the reporting month is tabulated in **Table I**.

**Table I Summary Table for Non-compliance Recorded in the Reporting Month**

Monitored By	Monitoring Station	Parameter	No. of Exceedance		No. of Exceedance Due to the Project		Action Taken
			Action Level	Limit Level	Action Level	Limit Level	
DC/2009/10	NM5	Noise	0	0	0	0	N/A
	NM6	Noise	0	0	0	0	N/A
	AM7	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A
	AM8	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A
	AM6b	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A

*1-hour TSP Monitoring*

5. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

*24-hour TSP Monitoring*

6. All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

*Construction Noise*

7. All construction noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

**Environmental Licenses and Permits**

8. Licenses/Permits granted to the Project include the Environmental Permit (EP); Billing account for Disposal of Construction Waste, Registered as Chemical Waste Producer.

**Environmental Mitigation Implementation Schedule**

9. According to the EIA Report Section 3.74, 4.56 and 13.44, air quality, noise and landscape and visual would be the key environmental issues and mitigation measures shall be implemented during the construction phase. Details of the implementation of mitigation measures are provided in the **Appendix J**.

**Key Information in the Reporting Month**

10. Summary of key information in the reporting month is tabulated in **Table II**.

**Table II Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Report for March 2021	Submitted on 14 April 2021	No Comment	---
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---

**Summary of Complaints and Prosecutions**

11. No environmental complaint and prosecution was received for the Project in the reporting month.
12. There were no environmental complaint and prosecution received since the commencement of the Project. The Complaint Log is presented in **Appendix K**.

**Future Key Issues:**

13. Major site activities for the coming two months include:

DOU3

- Reliability test for DOU3
- Pre-handover inspection for DOU3

MPS2

- Handover of upgraded pumps (#1 - #8)
- Defect rectification

CEPT Tank

- Handover of CEPT

14. The environmental concerns in the coming months are mainly on construction waste and general refuse storage.



## 1. INTRODUCTION

### Background

- 1.1 The Project ‘HATS Stage 2A - Upgrading works at Stonecutters Island Treatment Works (SCISTW) – Main Pumping Station, Sedimentation Tanks and Ancillary Facilities’ under Contract No: DC/2009/10 mainly comprises the construction of a large underground pumping station with an internal diameter of 55 metres and a depth of more than 40 metres, the provision of additional double-tray sedimentation tanks, a new computer control system, the expansion and modification of existing installations of the SCISTW as well as the construction of other ancillary facilities. The general location plan of the Project is shown in **Figure 1**.
- 1.2 The Project is under Harbour Area Treatment Scheme (HATS) Stage 2A and is a designated project with Register No. : AEIAR-121/2008. The current works under the Project at SCISTW for HATS 2A are covered by the Environmental Permit (Permit No. EP-322/2008/G), which was issued on 9<sup>th</sup> May 2014 by the Environmental Protection Department (hereinafter called EPD) to the Drainage Services Department (hereinafter called the DSD) as the Permit Holder.
- 1.3 Sun Fook Kong - Bestwise Joint Venture (hereafter called the SBJV) was commissioned by the DSD to undertake the construction of the Contract No. DC/2009/10 “HATS 2A –Upgrading works at Stonecutters Island Treatment Works – Main Pumping, Sedimentation Tanks and Ancillary Facilities”. The date of commencement of construction of the Project is 24<sup>th</sup> February 2011.
- 1.4 Wellab Limited was commissioned by SBJV to undertake the Environmental Monitoring and Audit (EM&A) works for the project and was appointed as the Environmental Team (ET) of the Project under Condition 2.1 of the EP. The date of commencement of EM&A works is 14<sup>th</sup> April 2011. The Project cover the environmental monitoring works at monitoring stations AM6b, AM7, AM8, NM5 and NM6.
- 1.5 This is the 121<sup>st</sup> monthly EM&A report summarizing the EM&A works conducted for the Project in April 2021.

### Project Organizations

- 1.6 The contacts of the Project are shown in **Table 1.1** and the organization chart of ET for Contract is shown in **Figure 2**.

**Table 1.1 Key Project Contacts**

Party	Role	Name	Position	Phone No.
Ove Arup & Partners Hong Kong Ltd	Engineer’s Representative	Mr. M P Gamini Ananda	Senior Resident Engineer	6049 5561
	Coordinator	Mr. Kevin Cheung	Resident Engineer	6049 5562
Wellab	Environmental Team	Dr. Priscilla Choy	ET Leader	2151 2089
		Mr. Howard Chan	Project Coordinator & Audit Team	2151 2073

Party	Role	Name	Position	Phone No.
Mott MacDonald	Independent Environmental Checker	Dr. Anne Kerr	Independent Environmental Checker	2828 5757
Sun Fook Kong - Bestwise Joint Venture	Contractor	Mr. Keith Ho	Site Agent	2620 0070
		Mr. Albus Cheung	Environmental Officer	2620 0070

### Summary of EM&A Requirements

- 1.7 The EM&A programme requires construction phase monitoring for air quality and construction noise, landscape and visual and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
- All monitoring parameters;
  - Action and Limit levels for all environmental parameters;
  - Event Action Plans;
  - Environmental mitigation measures, as recommended in the project EIA study final report; and
  - Environmental requirements in contract documents.
- 1.8 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in **Section 4** of this report.
- 1.9 This report presents the monitoring results, observations, locations, equipment, period, for required monitoring parameter namely air quality, noise and audit works conducted for the Project in April 2021.

## 2. AIR QUALITY

### Monitoring Requirements

- 2.1 1-hour and 24-hour TSP monitoring were conducted to monitor the air quality. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

### Monitoring Locations

- 2.2 Three designated monitoring stations, AM6b, AM7 and AM8 were selected for impact dust monitoring for the Project. The previous location of AM6a was not available for future monitoring due to no secured power supply for operation and therefore the previous location of AM6a was relocated to the monitoring station AM6b on 20<sup>th</sup> October 2020 after handover of part of Portion 7. **Table 2.1** describes the air quality monitoring locations, which are also depicted in **Figure 1**.

**Table 2.1 Locations for Air Quality Monitoring**

Monitoring Station	Monitored by	Location of Measurement
AM6b <sup>(1)</sup>	DC/2009/10	Works site boundary
AM7		North West Kowloon Sewage Pumping Station
AM8		Block A of Government Dockyard

Remark:

(1) AM6b – The previous location of AM6a was relocated after handover of part of Portion 7.

### Monitoring Equipment

- 2.3 **Table 2.2** summarizes the air quality monitoring equipment and **Appendix B** shows the copies of calibration certificates for the equipment at AM6b, AM7 and AM8.

**Table 2.2 Air Quality Monitoring Equipment**

Equipment	Model and Make	Quantity
Laser Dust Monitor	Met One Instruments no. AEROCET-831	5
HVS Sampler	TISCH: Model no. TE-5170	3
Calibrator	TISCH: Model TE-5025A	2

### Monitoring Parameters, Frequency and Duration

- 2.4 **Table 2.3** summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period. The air quality monitoring schedule for AM6b, AM7 and AM8 are shown in **Appendix C**.

**Table 2.3 Impact Dust Monitoring Parameters, Frequency and Duration**

Monitoring Station	Parameter	Period	Frequency
All monitoring locations	1-hour TSP	0700-1900 hrs	3 times/ every 6 days
	24-hour TSP	0000-2400 hrs	once in every 6 days

### Monitoring Methodology and QA/QC Procedure

- 2.5 The monitoring methodology and QA/QC procedures for monitoring station AM6b,

---

AM7 and AM8 are presented as follow:

- 2.6 The general weather conditions (i.e. sunny, cloudy or rainy) were recorded by the field staff's observation on the monitoring day.

*TSP Monitoring with Laser Dust Monitor*

Measuring Procedures

- 2.7 The measuring procedures of the 1-hour dust meters were in accordance with the Manufacturer's Instruction Manual as follows:
- The 1-hour dust meter is placed at least 1.3 meters above ground.
  - Remove the red rubber cap from the AEROCET-831 inlet nozzle.
  - Turn on the power switch that is located on the right side of the AEROCET-831.
  - On power up the product intro screen is displayed for 3 seconds. The intro screen displays the product name and firmware version.
  - Then the main counter screen will be displayed.
  - Press the START button. Internal vacuum pump start running. After 1 minute the pump will stop and the 0.5 $\mu$ m and 5 $\mu$ m channels will show the cumulative counts of particles larger than 0.5 $\mu$ m and 5 $\mu$ m per cubic foot.
  - The AEROCET-831 is now checked out and ready for use.
  - To switch off the AEROCET-831 power to stop the measuring after 1 hour sampling.
  - Information such as sampling date, time, and display value and site condition were recorded during the monitoring period.

Maintenance/Calibration

- 2.8 The following maintenance/calibration was required for the direct dust meters:
- Check the meter at a 3-month interval and calibrate the meter at a 1-year interval throughout all stages of the air quality monitoring.

*TSP Monitoring with High Volume Sampler*

Instrumentation

- 2.9 High Volume Sampler (HVS) completed with appropriate sampling inlets was employed for air quality monitoring. Each sampler comprised of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

***HVS Installation***

- 2.10 The following guidelines were adopted during the installation of HVS:
- Sufficient support was provided to secure the samplers against gusty wind.
  - No two samplers were placed less than 2 meters apart.
  - The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
  - A minimum of 2 meters of separation from walls, parapets and penthouses was required for rooftop samples.
  - A minimum of 2 meters separation from any supporting structure, measured horizontally was required.

- No furnaces or incineration flues were nearby.
- Airflow around the sampler was unrestricted.
- The samplers were more than 20 meters from the drip line.
- Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.

### ***Filters Preparation***

- 2.11 Fibre glass filters, which have a collection efficiency of larger than 99% of particles of 0.3  $\mu\text{m}$  in diameter, were used. A HOKLAS accredited laboratory, Wellab Ltd., was responsible for the preparation of 24-hr conditioned and pre-weighed filter papers for Wellab's monitoring team.
- 2.12 All filters, which were prepared by Wellab Ltd., were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was < 50% and not variable by more than  $\pm 5\%$ . A convenient working RH was 40%.
- 2.13 Wellab Ltd. has a comprehensive quality assurance and quality control programme.

### ***Operating/Analytical Procedures***

- 2.14 Operating/analytical procedures for the air quality monitoring were highlighted as follows:
- Prior to the commencement of the dust sampling, the flow rate of the HVS was properly set (between 1.1  $\text{m}^3/\text{min.}$  and 1.4  $\text{m}^3/\text{min.}$ ) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.
  - The power supply was checked to ensure the sampler worked properly.
  - On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air quality monitoring station.
  - The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centred with the stamped number upwards, on a supporting screen.
  - The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
  - The shelter lid was closed and secured with the aluminium strip.
  - The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
  - After sampling, the filter was removed and sent to the Wellab Ltd. for weighing. The elapsed time was also recorded.
  - Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than  $\pm 3$ °C; the relative humidity (RH) should be < 50% and not vary by more than  $\pm 5\%$ . A convenient working RH is 40%. Weighing results were returned to Wellab for further analysis of TSP concentrations collected by each filter.

**Maintenance/Calibration**

2.15 The following maintenance/calibration was required for the HVS:

- The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.

**Results and Observations**

2.16 **Table 2.4** summarizes the monitoring results at AM6b, AM7 and AM8 in the reporting month.

**Table 2.4 Summary of 1-hour and 24-hour TSP Monitoring Result in the Reporting Month**

Air Quality Monitoring Station	Average $\mu\text{g}/\text{m}^3$	Range $\mu\text{g}/\text{m}^3$	Action Level $\mu\text{g}/\text{m}^3$	Limit Level $\mu\text{g}/\text{m}^3$
1 hour TSP				
AM6b	202	80 – 294	346	500
AM7	107.8	55.5 – 162.2	322	
AM8	86.7	45.7 – 125.4	307	
24 hours TSP				
AM6b	73	27 – 107	196	260
AM7	56	42 – 79	207	
AM8	61	47 – 79	158	

- 2.17 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. Summary of exceedance is presented in **Appendix F**.
- 2.18 All 24-hr TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded. Summary of exceedance is presented in **Appendix F**.
- 2.19 The details and graphical presentations of the air quality monitoring results at AM6b, AM7 and AM8 are shown in **Appendix D**.
- 2.20 According to field observations during site inspection, the identified dust sources at the monitoring stations were mainly from vehicles movement and construction activities from other Contract in the site.

### 3. NOISE

#### Monitoring Requirements

- 3.1 Two noise monitoring stations, namely NM5 and NM6 was designated in the EM&A Manual for impact monitoring. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.
- 3.2 Monitoring station (NM6) serves as an alternative location for FSD Diving Rescue and Diving Training Centre which is regarded as a Noise Sensitive Receiver (NSR) as it is an institution. Monitoring station (NM6) was set up at the proposed location in accordance with the Monitoring Proposal submitted by ET of Contract DC/2009/05, as agreed by the ER and IEC.

#### Monitoring Locations

- 3.3 Noise monitoring was conducted at two designated monitoring stations as listed in **Table 3.1**.

**Table 3.1 Location of Noise Monitoring Stations**

Monitoring Station	Monitored By	Location of Measurement
NM5	DC/2009/10	Near FSD Diving Rescue and Training Centre
NM6		Customs' Marine Base (Block H of Government Dockyard Rooftop)

#### Monitoring Equipment

- 3.4 **Table 3.2** summarizes the noise quality monitoring equipment and **Appendix B** shows the copies of calibration certificates for the equipment used at NM5 and NM6 in the reporting month.

**Table 3.2 Noise Monitoring Equipment**

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	BSWA, Model no.: BSWA 308 SVANTEK, Model no: SVAN 957	3
Calibrator	SVANTEK, Model no: SV 30A Bruel & Kjaer, Model no: 4231	3

#### Monitoring Parameters, Frequency and Duration

- 3.5 **Table 3.3** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule of the reporting month for NM5 and NM6 is shown in **Appendix C**.

**Table 3.3 Noise Monitoring Parameters, Frequency and Duration**

Monitoring Stations	Parameter	Period	Frequency
NM5 NM6	$L_{eq}(30 \text{ min.})$ dB(A)	0700-1900 hrs. on weekdays	Once per week
	$L_{eq}(5 \text{ min.})$ dB(A)	During restricted hours	Monitoring to be conducted when construction works were to be carried out

**Monitoring Methodology and QA/QC Procedures**

- 3.6 The monitoring methodology and QA/QC procedure at NM5 and NM6 are presented as follow:
- 3.7 General weather conditions (i.e. sunny, cloudy or rainy) were recorded by field observation during equipment checking and estimated according to weather data from the Hong Kong Observatory.

**Field Monitoring**

- 3.8 The monitoring procedures are as follows:
- The Sound Level Meter was set on a tripod at a height of 1.2 m above the ground.
  - For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels were adjusted with a correction of +3 dB(A).
  - The battery condition was checked to ensure good functioning of the meter.
  - Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
    - Frequency weighting : A
    - Time weighting : Fast
    - Measurement time : 30 minutes
  - Prior to and after noise measurement, the meter was calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
  - Noise monitoring was carried out 30 minutes during on the monitoring days. Monitoring data was recorded and stored automatically within the sound level meter system. At the end of the monitoring period, noise levels in term of  $L_{eq}$ ,  $L_{90}$  and  $L_{10}$  were recorded.
  - All the monitoring data within the sound level meter system was downloaded through the computer software, and all these data was checked and reviewed within the computer.



***Maintenance and Calibration***

3.9 Maintenance and Calibration procedures were as follows:

- The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator were checked and calibrated at yearly intervals.

**Results and Observations**

3.10 **Table 3.4** summarizes the monitoring results at NM5 and NM6 in the reporting month.

**Table 3.4 Summary the Noise Monitoring Results in Reporting Month**

For the time period 0700-1900 hrs. on weekdays		
Noise Monitoring Station	Range, dB(A) L <sub>eq</sub> (30 min.)	Limit Level dB(A)
NM5	58.2 – 66.0	75.0
NM6	56.3 – 69.3	75.0

3.11 The construction noise monitoring at the designated location was conducted by the ET of Contracts DC/2009/10 as scheduled in the reporting month. The monitoring results and graphical presentations could be referred to **Appendix E**.

3.12 1900-2300 hours noise monitoring was not conducted in the reporting month as there were no construction works during the period of restricted hours.

3.13 No Action/Limit Level exceedance was recorded in the reporting month. Summary of exceedance is presented in **Appendix F**.

3.14 The major noise sources identified at the designated noise monitoring stations were vehicle movement and construction activities from other Contract in Stonecutters Island STW.

**4. ENVIRONMENTAL AUDIT****Site Audits**

- 4.1 Site audits were conducted on a weekly basis to monitor the implementation of environmental management practices and mitigation measures at the site area by the Contractor.
- 4.2 Site inspections were undertaken to ensure and check that the implementation and maintenance of mitigation measures for Air Quality, Noise, Water Quality, Waste Management, Landscape and Visual are being properly carried out in the reporting month in accordance to section 14.1 of the EM&A Manual. No non-compliance was observed during the site inspections.
- 4.3 The summaries of site audits are attached in **Appendix G**.

**Implementation Status of Environmental Mitigation Measures**

- 4.4 Details of the implementation of mitigation measures are provided in the **Appendix J**.
- 4.5 During the weekly environmental site inspections in the reporting period, no non-conformance was identified. The observations of the site audit for the Projects are summarized in **Table 4.1**.

**Table 4.1 Observations of Site Audit**

<b>Parameters</b>	<b>Ref. Number</b>	<b>Observations</b>	<b>Follow Up Action</b>
<b>Water Quality</b>	N/A	There was no observation in the reporting month.	N/A
<b>Air Quality</b>	N/A	There was no observation in the reporting month.	N/A
<b>Waste/ Chemical Management</b>	N/A	There was no observation in the reporting month.	N/A
<b>Landscape and Visual</b>	N/A	There was no observation in the reporting month.	N/A
<b>Noise</b>	N/A	There was no observation in the reporting month.	N/A
<b>Permit/ Licenses</b>	N/A	There was no observation in the reporting month.	N/A

**Review of Environmental Monitoring Procedures**

- 4.6 The monitoring works conducted by Contract DC/2009/10's ET were reviewed at a regular basis to ensure the monitoring procedures were carried out properly.

**Status of Environmental Licensing and Permitting**

- 4.7 All permits/licenses obtained for the Contract DC/2009/10 are summarized in **Table 4.2**.

**Table 4.2 Summary of Environmental Licence / Permit for DC/2009/10**

Reference Number	Valid Period		Details	Status
	From	To		
<b><i>Water Discharge License</i></b>				
WT00024404-2016	19/5/2016	31/5/2021	The application was approved on 19-5-2016.	Valid
WT00025973-2016	22/11/2016	31/5/2021	The application was approved on 22/11/2016.	Valid
<b><i>Registered Chemical Waste Producer</i></b>				
WPN5213-269-3584-01	N/A	N/A	The application was approved on 4-5-2011.	Valid
<b><i>Billing Account for Disposal of Construction Waste</i></b>				
CSW01444	16/3/2011	N/A	The application was approved on 16-3-2011.	Valid
<b><i>Notification of Works Under APCO</i></b>				
327427	N/A	N/A	Notice form received by EPD on 2-3-2011.	N/A

**Status of Waste Management**

- 4.8 The amount of wastes generated by the activities of the Project in the reporting month is shown in **Appendix H**.

**Implementation Status of Event Action Plans**

- 4.9 The Event Action Plans for air quality and noise are presented in **Appendix I**.

1-hr TSP

- 4.10 No Action/Limit Level exceedance was recorded.

24-hr TSP

- 4.11 No Action/Limit Level exceedance was recorded.

Construction Noise

- 4.12 No Action/Limit Level exceedance was recorded.

Landscape and Visual

- 4.13 No major deficiency was recorded.

**Summary of Complaints and Prosecutions**

- 4.14 No environmental complaint and prosecution was received for the Project in the reporting month.
- 4.15 There were no environmental complaint and prosecution received since the commencement of the Project. The Complaint Log is presented in **Appendix K**.

## **5. FUTURE KEY ISSUES**

### **Key Issues for the Coming Month**

5.1 Key environmental issues in the coming month include:

- Disposal/ Storage of general refuse and construction waste on-site;

### **Monitoring Schedule for the Next Month**

5.2 The tentative environmental monitoring schedule over the next month is shown in **Appendix C** of this report.

### **Construction Program for the Next Month**

5.3 The tentative construction program is provided in **Appendix L**.

## 6. CONCLUSIONS AND RECOMMENDATIONS

### Conclusions

- 6.1 Environmental monitoring and audit works were performed in the reporting month and all monitoring results were checked and reviewed.

#### 1-hour TSP Monitoring

- 6.2 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### 24-hour TSP Monitoring

- 6.3 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Construction Noise Monitoring

- 6.4 All Construction Noise monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

#### Environmental Audit

- 6.5 Environmental site audits were conducted as weekly basis in the reporting month. No non-compliance was recorded.

#### Complaint and Prosecution

- 6.6 No environmental complaint and prosecution was received in the reporting month.

### Recommendations for next reporting month

- 6.7 The following recommendations were made for the next report month:

#### *Water Quality*

- To avoid water accumulation on site and carry out larviciding against mosquito breeding for stagnant water when mosquito larvae are observed.

#### *Waste/Chemical Management*

- To provide proper rubbish bins / skips for waste collection;
- To check for any accumulation of wasted materials or rubbish on site;
- To provide adequate chemical waste storage area on site;
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the equipment; and
- To avoid improper handling or storage of oil drum and cement on site.

#### *Landscape and Visual*

- To avoid any construction materials being placed inside the tree protection zone.


---

---

## FIGURES


---

---

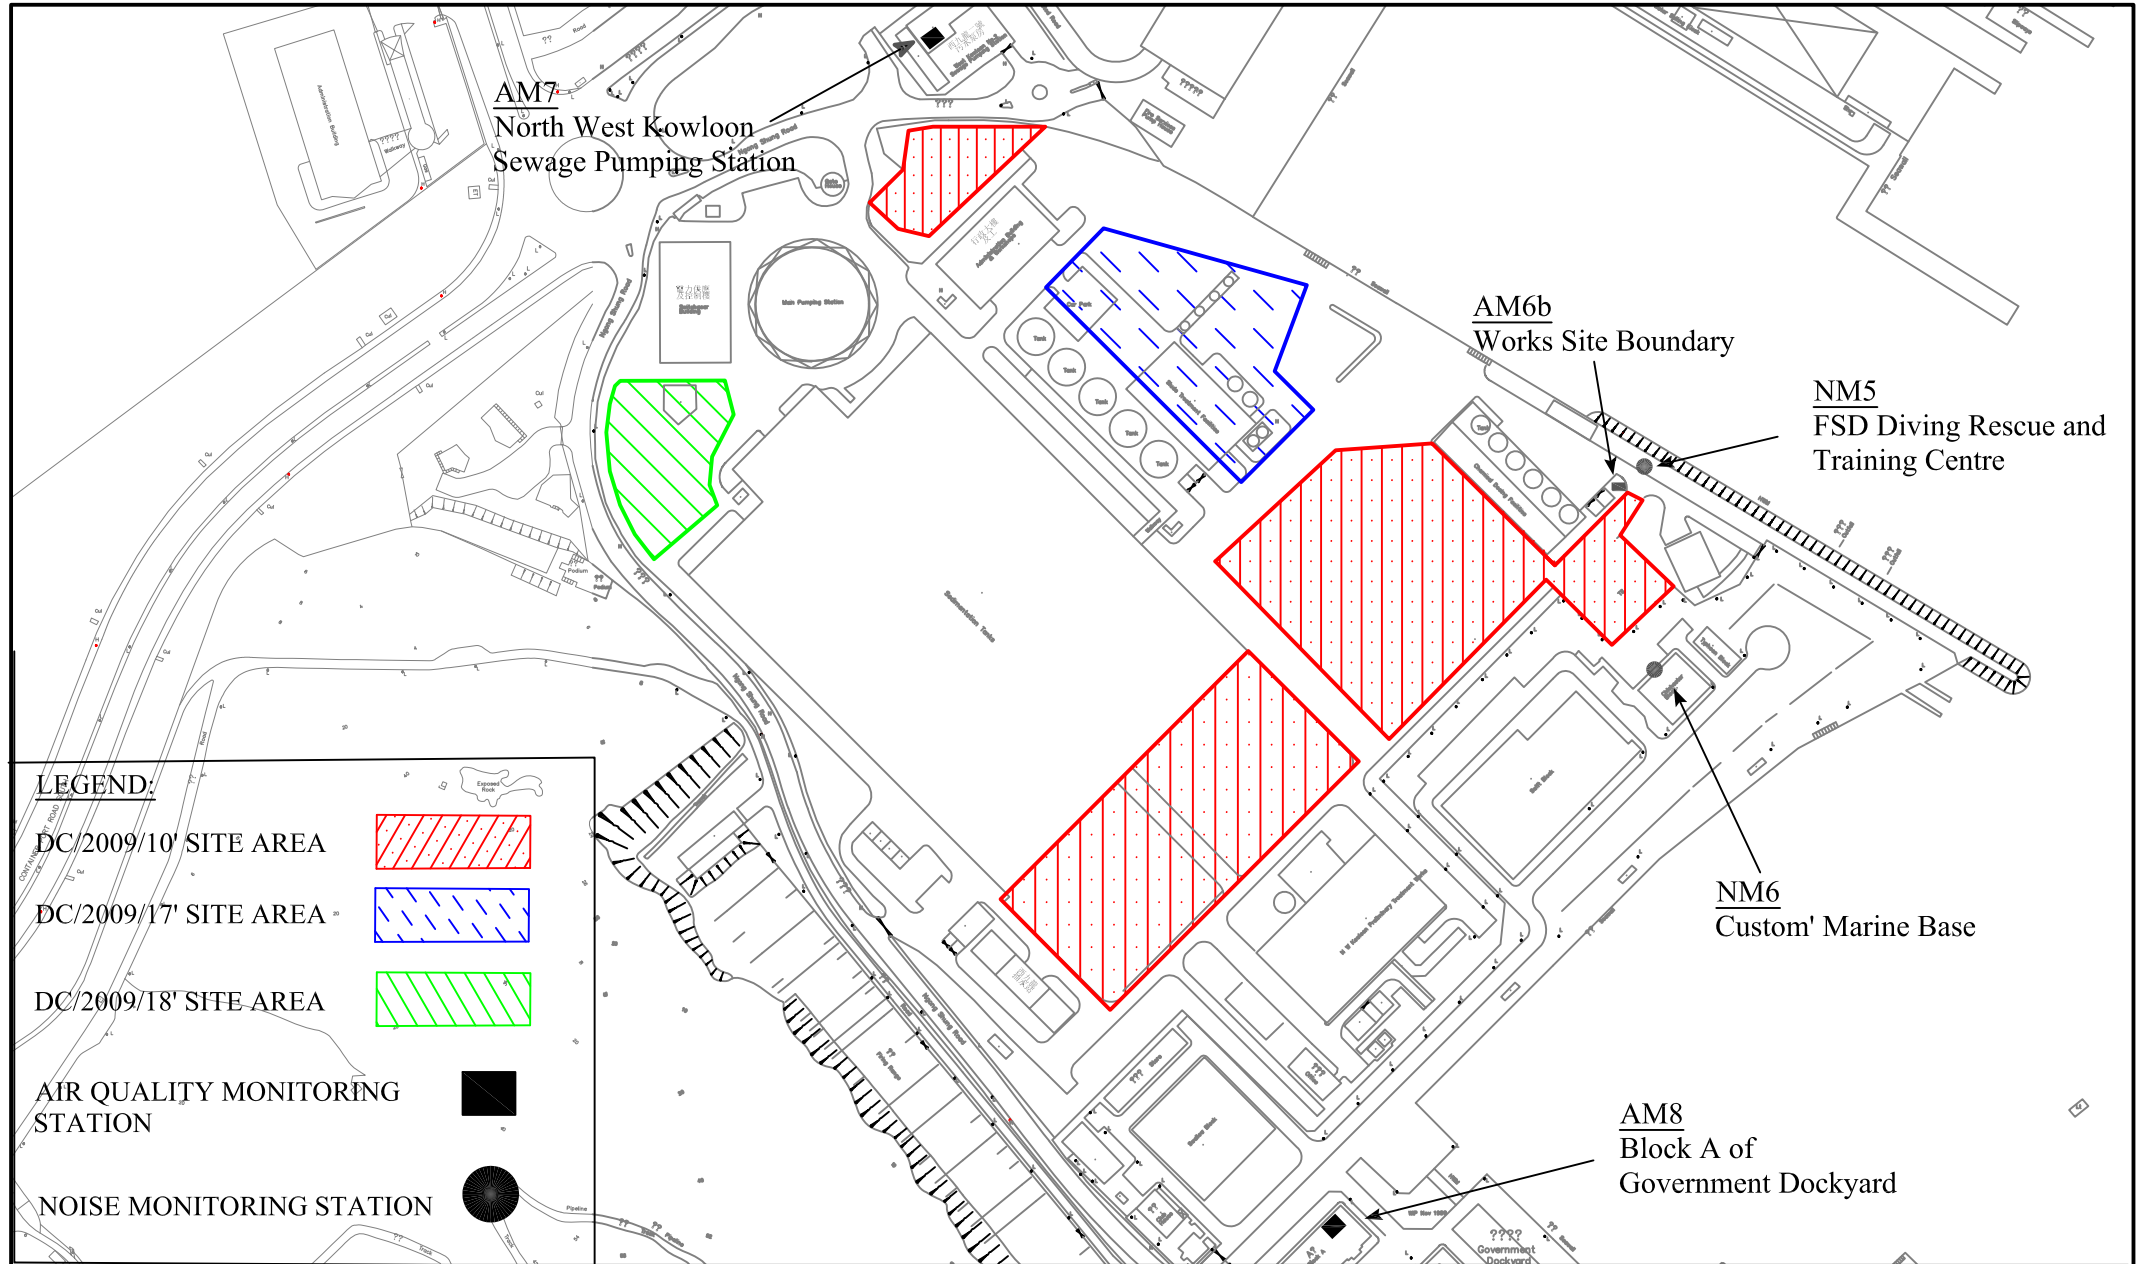

**LEGEND:**

- DC/2009/10' SITE AREA
- DC/2009/17' SITE AREA
- DC/2009/18' SITE AREA



AIR QUALITY MONITORING STATION



NOISE MONITORING STATION





Contractor No. DC/2009/10  
 HATS 2A - Upgrading Main Pumping Station, Sedimentation Tank and Ancillary Facilities at SCISTW

General Location Plan of the Project and Location of Air Quality and Noise Monitoring Stations



SCALE	A4@ 1:8000	DATE	Nov 2020
CHECK	—	DRAWN	HC
Project No.	MA11007	FIGURE NO.	1
		REV	—

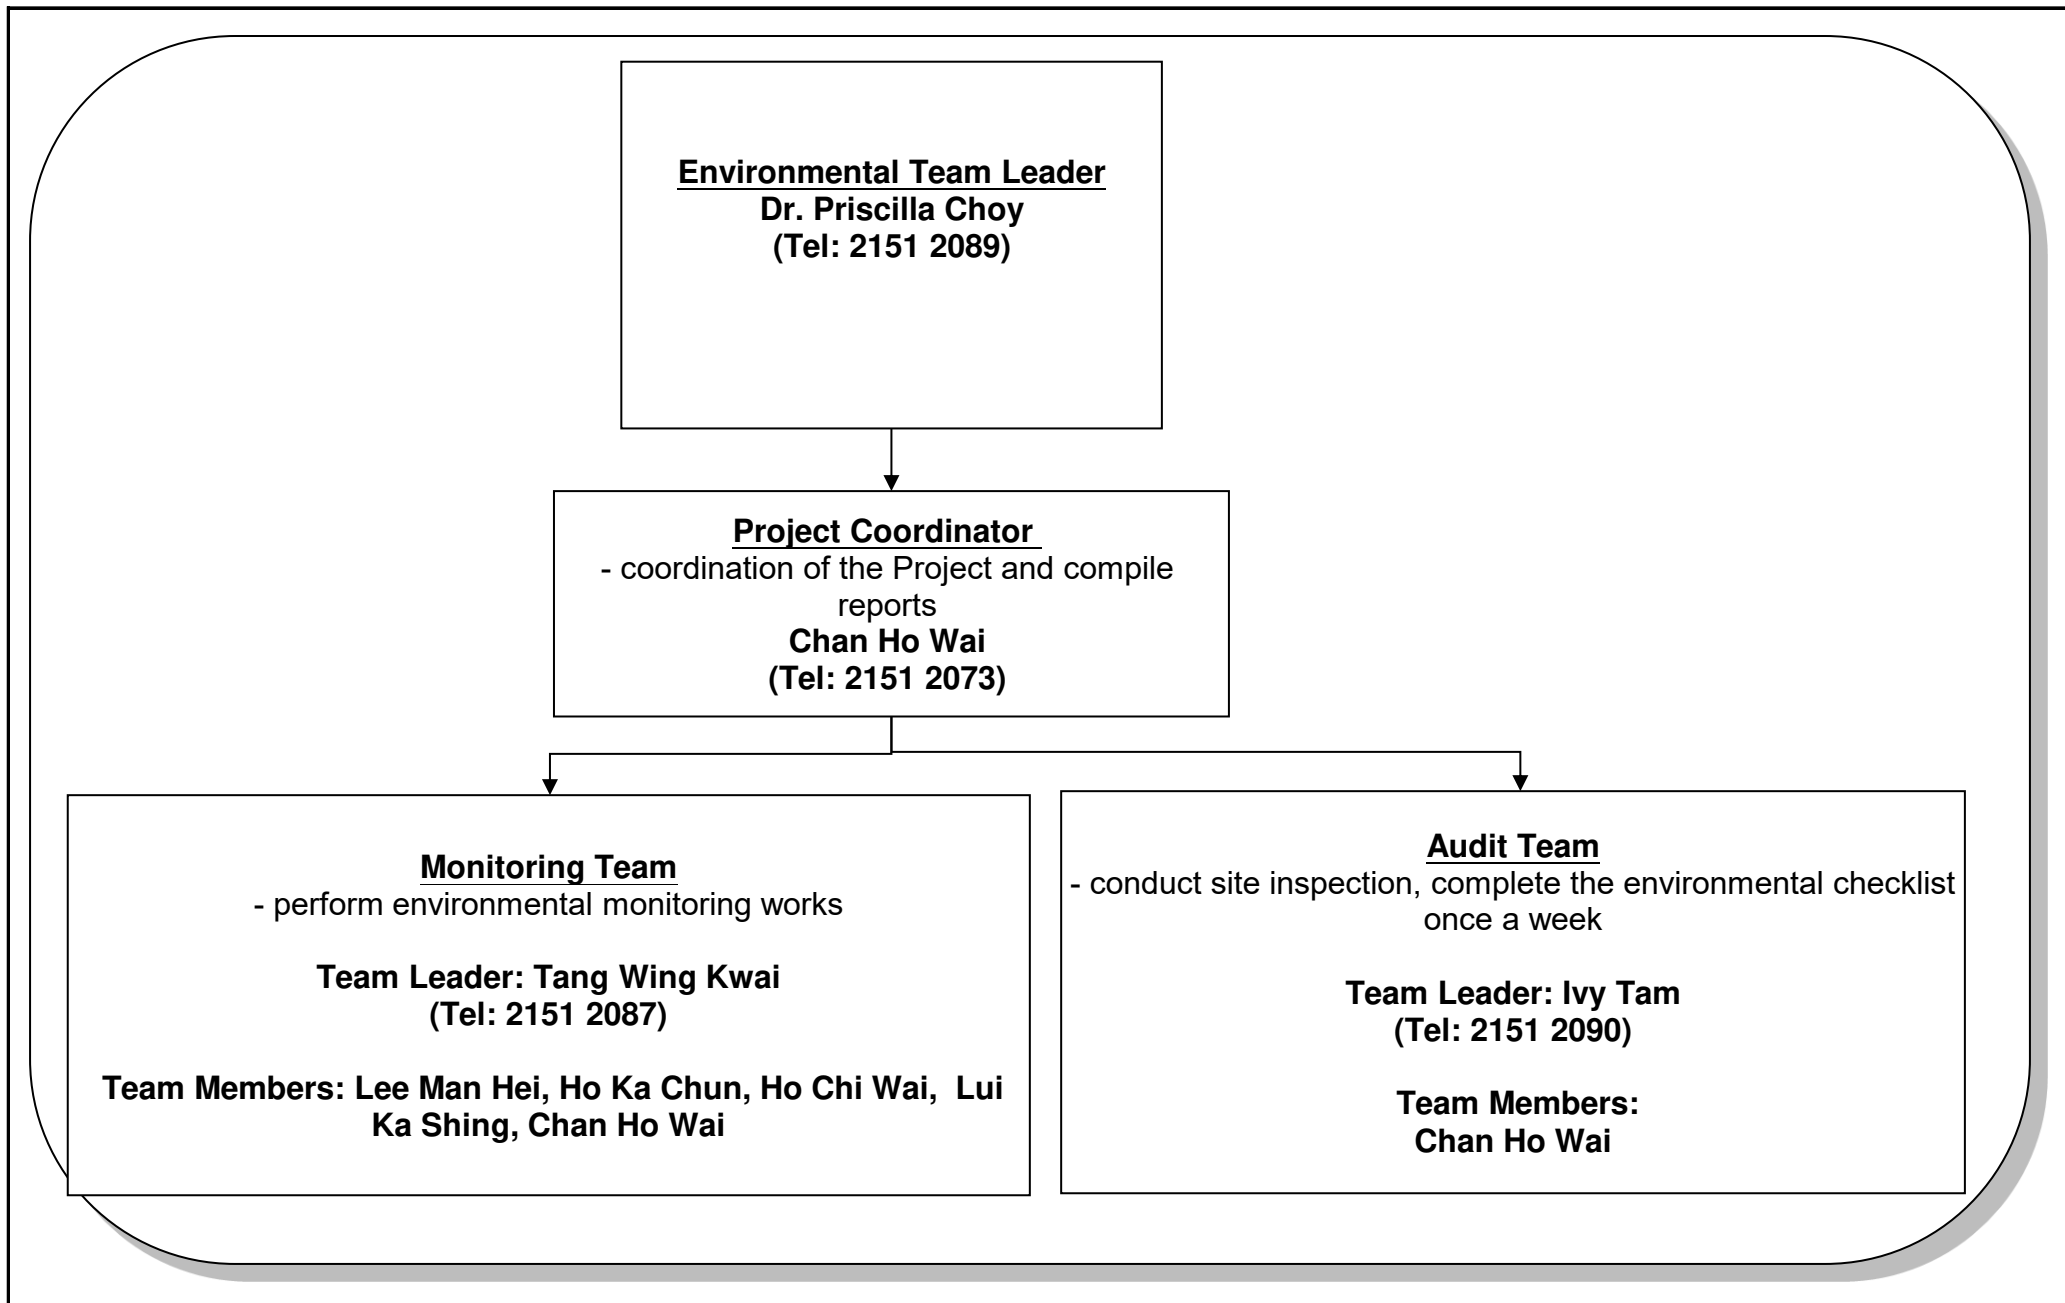

Title	Contract No. DC/2009/10 HATS Stage 2A – Upgrading Works at SISTW Main Pumping Station, Sedimentation Tanks and Ancillary Facilities ET's Organization Chart	Scale N.T.S Version v.2	Project No. MA11007 Figure 2	
-------	--	----------------------------------	---------------------------------------	---



---

---

**APPENDIX A  
ACTION AND LIMIT LEVELS FOR AIR  
QUALITY AND NOISE QUALITY**

---

---

## Appendix A Action and Limit Levels

**Table A-1 Action and Limit Levels for 1-Hour TSP and 24-Hour TSP**

Monitoring Stations	Action Level ( $\mu\text{g}/\text{m}^3$ )		Limit Level ( $\mu\text{g}/\text{m}^3$ )	
	1-hour	24-hour	1-hour	24-hour
AM6b	346	196	500	260
AM7	322	207	500	260
AM8	307	158	500	260

**Table A-2 Action and Limit Level for Construction Noise**

Monitoring Stations	Time Period	Action Level	Limit Level in dB(A)
NM5 NM6	0700-1900 hours on normal weekdays	When one documented complaint is received	75
	Evening Time of normal weekdays and General Holidays:  All days during the evening (1900 to 2300 hours), and general holidays (including Sundays) during the day-time and evening (0700 to 2300 hours)	N/A	70 <sup>(1)</sup>

Notes: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

---

---

**APPENDIX B  
COPIES OF CALIBRATION  
CERTIFICATES**

---

---

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34871A
Date of Issue:	2021-03-03
Date Received:	2021-03-01
Date Tested:	2021-03-01
Date Completed:	2021-03-03
Next Due Date:	2021-05-02
Page:	1 of 1

**ATTN:** Ms. Meiling Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : Dust Monitor  
 Manufacturer : Met One Instruments  
 Model No. : AEROCET-831  
 Serial No. : X23808  
 Flow rate : 0.1 cfm  
 Zero Count Test : 0 count per 1 minute  
 Equipment No. : WA-01-02

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
 Relative Humidity : 40-70%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Tisch Environmental Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	1.131
-------------------------	-------

\*\*\*\*\*

PREPARED AND CHECKED BY:  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
 General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34870
Date of Issue:	2021-03-01
Date Received:	2021-02-27
Date Tested:	2021-02-27
Date Completed:	2021-03-01
Next Due Date:	2021-04-30
Page:	1 of 1

**ATTN:** Ms. Meiling Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : Dust Monitor  
 Manufacturer : Met One Instruments  
 Model No. : AEROCET-831  
 Serial No. : X24476  
 Flow rate : 0.1 cfm  
 Zero Count Test : 0 count per 1 minute  
 Equipment No. : WA-01-05

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
 Relative Humidity : 40-70%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Tisch Environmental Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	1.148
-------------------------	-------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34871D
Date of Issue:	2021-03-03
Date Received:	2021-03-01
Date Tested:	2021-03-01
Date Completed:	2021-03-03
Next Due Date:	2021-05-02

Page: 1 of 1

**ATTN:** Ms. Meiling Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : Dust Monitor  
Manufacturer : Met One Instruments  
Model No. : AEROCET-831  
Serial No. : X24475  
Flow rate : 0.1 cfm  
Zero Count Test : 0 count per 1 minute  
Equipment No. : WA-01-07

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
Relative Humidity : 40-70%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Tisch Environmental Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	1.096
-------------------------	-------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1808, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	35071C
Date of Issue:	2021-04-26
Date Received:	2021-04-23
Date Tested:	2021-04-24
Date Completed:	2021-04-26
Next Due Date:	2021-06-25
Page:	1 of 1

**ATTN:** Ms. Meiling Tang

**Certificate of Calibration**

**Item for Calibration:**

Description	: Dust Monitor
Manufacturer	: Met One Instruments
Model No.	: AEROCET-831
Serial No.	: X23811
Flow rate	: 0.1 cfm
Zero Count Test	: 0 count per 1 minute
Equipment No.	: WA-01-09

**Test Conditions:**

Room Temperature	: 17-22 degree Celsius
Relative Humidity	: 40-70%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Tisch Environmental Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	1.135
-------------------------	-------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34870D
Date of Issue:	2021-03-01
Date Received:	2021-02-27
Date Tested:	2021-02-27
Date Completed:	2021-03-01
Next Due Date:	2021-04-30
Page:	1 of 1

**ATTN:** Ms. Meiling Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : Dust Monitor  
 Manufacturer : Met One Instruments  
 Model No. : AEROCET-831  
 Serial No. : X24478  
 Flow rate : 0.1 cfm  
 Zero Count Test : 0 count per 1 minute  
 Equipment No. : WA-01-10

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
 Relative Humidity : 40-70%

**Test Specifications & Methodology:**

1. Instruction and Operation Manual High Volume Sampler, Tisch Environmental Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

**Results:**

Correlation Factor (CF)	1.139
-------------------------	-------

\*\*\*\*\*

*PREPARED AND CHECKED BY:*  
For and On Behalf of **WELLAB Ltd.**

  
\_\_\_\_\_  
**PATRICK TSE**  
General Manager



**High-Volume TSP Sampler  
5-POINT CALIBRATION DATA SHEET**

File No. MA11007/WA12/0005

Station AM6 - Works Site Boundary Operator: HL  
 Date: 11-Feb-21 Next Due Date: 10-Apr-21  
 Equipment No.: WA-12-12 Serial No. 2355

Ambient Condition			
Temperature, Ta (K)	292	Pressure, Pa (mmHg)	762.6

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0588	Intercept, bc	-0.02681
Last Calibration Date:	18-Feb-20	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	18-Feb-21	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.4	3.56	61.06	8.1	2.88
2	10.8	3.33	57.02	7.4	2.75
3	7.8	2.83	48.52	5.1	2.29
4	5.7	2.42	41.55	3.7	1.95
5	3.2	1.81	31.24	2.3	1.53

**By Linear Regression of Y on X**  
 Slope, mw = 0.0466 Intercept, bw = 0.0512  
 Correlation coefficient\* = 0.9978  
 \*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM  
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point;  $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.12

Remarks: \_\_\_\_\_

Conducted by: LEE MAN KEI Signature: Lee Date: 11-2-2021  
 Checked by: wk. Tang Signature: Kwan Date: 11/2/2021

**High-Volume TSP Sampler**  
**5-POINT CALIBRATION DATA SHEET**

File No. MA11007/WA12/0006

Station AM6 - Works Site Boundary Operator: HL  
Date: 8-Apr-21 Next Due Date: 7-Jun-21  
Equipment No.: WA-12-12 Serial No. 2355

Ambient Condition			
Temperature, Ta (K)	296.8	Pressure, Pa (mmHg)	762.9

Orifice Transfer Standard Information					
Serial No.	0993	Slope, mc	0.0569	Intercept, bc	-0.01398
Last Calibration Date:	28-Jan-21	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			
Next Calibration Date:	28-Jan-22				

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	13.1	3.63	64.13	8.4	2.91
2	10.7	3.28	57.98	6.5	2.56
3	7.6	2.77	48.90	4.9	2.22
4	5.8	2.42	42.75	3.6	1.90
5	3.6	1.90	33.73	2.4	1.56

**By Linear Regression of Y on X**

Slope, mw = 0.0441 Intercept, bw = 0.0491  
Correlation coefficient\* = 0.9979

\*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM  
From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W =  $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  3.75

Remarks: \_\_\_\_\_

Conducted by: [Signature] Signature: \_\_\_\_\_ Date: 8/4/21  
Checked by: [Signature] Signature: \_\_\_\_\_ Date: 8/4/21

**High-Volume TSP Sampler**  
**5-POINT CALIBRATION DATA SHEET**

File No. MA11007/WA14/0005

Station AM7 - North West Kowloon Sewage Pumping Station Operator: HL  
Date: 11-Feb-21 Next Due Date: 10-Apr-21  
Equipment No.: WA-12-14 Serial No. 2353

Ambient Condition			
Temperature, Ta (K)	291.4	Pressure, Pa (mmHg)	763.4

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0588	Intercept, bc	-0.02681
Last Calibration Date:	18-Feb-20	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			
Next Calibration Date:	18-Feb-21				

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.4	3.57	61.15	8.6	2.97
2	10.7	3.32	56.84	7.8	2.83
3	7.5	2.78	47.66	5.4	2.36
4	4.8	2.22	38.22	3.7	1.95
5	3.3	1.84	31.77	2.3	1.54

**By Linear Regression of Y on X**

Slope, mw = 0.0486 Intercept, bw : 0.0407  
Correlation coefficient\* = 0.9975

\*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W =  $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.41

Remarks: \_\_\_\_\_

Conducted by: LEE MAN HEI Signature: he Date: 11-2-2021  
Checked by: W.K. Tang Signature: Kwan Date: 11/2/2021

## High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

File No. MA11007/WA14/0006

Station AM7 - North West Kowloon Sewage Pumping Station Operator: HL  
 Date: 8-Apr-21 Next Due Date: 7-Jun-21  
 Equipment No.: WA-12-14 Serial No. 2353

Ambient Condition			
Temperature, Ta (K)	296.8	Pressure, Pa (mmHg)	762.9

Orifice Transfer Standard Information					
Serial No.	0993	Slope, mc	0.0569	Intercept, bc	-0.01398
Last Calibration Date:	28-Jan-21	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	28-Jan-22	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.4	3.54	62.40	8.6	2.94
2	10.3	3.22	56.89	7.4	2.73
3	7.7	2.79	49.22	5.3	2.31
4	4.9	2.22	39.32	3.5	1.88
5	3.2	1.80	31.82	2.5	1.59

**By Linear Regression of Y on X**

Slope, mw = 0.0453 Intercept, bw : 0.1195

Correlation coefficient\* = 0.9985

\*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W =  $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.24

Remarks: \_\_\_\_\_

Conducted by: LEE Man Ho Signature: \_\_\_\_\_  
 Checked by: Ho Ka Chun Signature: \_\_\_\_\_

Date: 8/4/2021  
 Date: 8/4/2021

**High-Volume TSP Sampler**  
**5-POINT CALIBRATION DATA SHEET**

File No. MA11007/WA18/005

Station AM8 - Block A of Government Dockyard Operator: HL  
Date: 11-Feb-21 Next Due Date: 10-Apr-21  
Equipment No.: WA-12-18 Serial No. 3219

Ambient Condition			
Temperature, Ta (K)	291.8	Pressure, Pa (mmHg)	763.1

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0588	Intercept, bc	-0.02681
Last Calibration Date:	18-Feb-20	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			
Next Calibration Date:	18-Feb-21				

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	12.3	3.55	60.86	8.0	2.86
2	10.8	3.33	57.05	6.7	2.62
3	7.9	2.85	48.86	5.2	2.31
4	5.4	2.35	40.48	3.6	1.92
5	3.6	1.92	33.13	2.4	1.57

**By Linear Regression of Y on X**

Slope, mw = 0.0455 Intercept, bw = 0.0704  
Correlation coefficient\* = 0.9986

\*If Correlation Coefficient < 0.990, check and recalibrate.

**Set Point Calculation**

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W =  $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.00

Remarks: \_\_\_\_\_

Conducted by: EFE MUMMER Signature: [Signature]  
Checked by: wk Tang Signature: [Signature]

Date: 11-2-2021  
Date: 11/2/2021

## High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

File No. MA11007/WA18/006

Station AM8 - Block A of Government Dockyard Operator: HL  
 Date: 8-Apr-21 Next Due Date: 7-Jun-21  
 Equipment No.: WA-12-18 Serial No. 3219

Ambient Condition			
Temperature, Ta (K)	296.8	Pressure, Pa (mmHg)	762.9

Orifice Transfer Standard Information					
Serial No.	0993	Slope, mc	0.0569	Intercept, bc	-0.01398
Last Calibration Date:	28-Jan-21	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	28-Jan-22	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	$\Delta H$ (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X-axis	$\Delta W$ (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	11.5	3.40	60.10	8.2	2.87
2	9.7	3.13	55.22	6.6	2.58
3	7.7	2.79	49.22	5.4	2.33
4	5.1	2.27	40.10	3.7	1.93
5	3.4	1.85	32.79	2.4	1.56

By Linear Regression of Y on X

Slope, mw = 0.0470 Intercept, bw : 0.0234  
 Correlation coefficient\* = 0.9987

\*If Correlation Coefficient < 0.990, check and recalibrate.

### Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM  
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point;  $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$  4.14

Remarks: \_\_\_\_\_

Conducted by: Lee Man Hei Signature: Lee Man Hei Date: 8/4/2021  
 Checked by: Ho Ka Chun Signature: Ho Ka Chun Date: 8/4/2021



<b>RECALIBRATION</b>
<b>DUE DATE:</b>
February 18, 2021

# Certificate of Calibration

Calibration Certification Information			
Cal. Date: February 18, 2020	Rootsmeter S/N: 438320	Ta: 294	°K
Operator: Jim Tisch		Pa: 753.1	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: <b>2896</b>		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4340	3.2	2.00
2	3	4	1	1.0230	6.4	4.00
3	5	6	1	0.9080	8.0	5.00
4	7	8	1	0.8680	8.8	5.50
5	9	10	1	0.7160	12.8	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
1.0001	0.6975	1.4173	0.9958	0.6944	0.8836
0.9959	0.9735	2.0044	0.9915	0.9692	1.2496
0.9937	1.0944	2.2410	0.9894	1.0896	1.3971
0.9927	1.1436	2.3504	0.9883	1.1386	1.4653
0.9873	1.3790	2.8347	0.9830	1.3729	1.7672
<b>QSTD</b>	m=	<b>2.07675</b>	<b>QA</b>	m=	<b>1.30043</b>
	b=	<b>-0.02681</b>		b=	<b>-0.01672</b>
	r=	<b>0.99993</b>		r=	<b>0.99993</b>

Calculations	
Vstd= $\Delta Vol \left( \frac{Pa - \Delta P}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)$	Va= $\Delta Vol \left( \frac{Pa - \Delta P}{Pa} \right)$
Qstd= $Vstd / \Delta Time$	Qa= $Va / \Delta Time$
For subsequent flow rate calculations:	
Qstd= $1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa= $1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



<b>RECALIBRATION</b>
<b>DUE DATE:</b>
January 28, 2022

# Certificate of Calibration

Calibration Certification Information			
Cal. Date: January 28, 2021	Rootsmeter S/N: 438320	Ta: 294	°K
Operator: Jim Tisch		Pa: 763.5	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: 0993		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4160	3.3	2.00
2	3	4	1	0.9980	6.4	4.00
3	5	6	1	0.8890	8.0	5.00
4	7	8	1	0.8500	8.8	5.50
5	9	10	1	0.7020	12.9	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H (Ta/Pa)}$ (y-axis)
1.0139	0.7160	1.4271	0.9957	0.7032	0.8776
1.0098	1.0118	2.0182	0.9916	0.9936	1.2411
1.0076	1.1334	2.2564	0.9895	1.1131	1.3875
1.0066	1.1842	2.3666	0.9885	1.1629	1.4553
1.0011	1.4261	2.8542	0.9831	1.4004	1.7551
<b>QSTD</b>	<b>m=</b>	<b>2.00902</b>	<b>QA</b>	<b>m=</b>	<b>1.25802</b>
	<b>b=</b>	<b>-0.01398</b>		<b>b=</b>	<b>-0.00860</b>
	<b>r=</b>	<b>0.99997</b>		<b>r=</b>	<b>0.99997</b>

Calculations	
Vstd= $\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va= $\Delta Vol((Pa-\Delta P)/Pa)$
Qstd= $Vstd/\Delta Time$	Qa= $Va/\Delta Time$
For subsequent flow rate calculations:	
$Qstd = 1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	$Qa = 1/m \left( \left( \sqrt{\Delta H (Ta/Pa)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
<b>Key</b>	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.  
 145 South Miami Avenue  
 Village of Cleves, OH 45002

[www.tisch-env.com](http://www.tisch-env.com)  
 TOLL FREE: (877)263-7610  
 FAX: (513)467-9009



**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	33962
Date of Issue:	2020-08-15
Date Received:	2020-08-13
Date Tested:	2020-08-13
Date Completed:	2020-08-15
Next Due Date:	2021-08-14
Page:	1 of 1

**ATTN:** Mr. W. K. Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : 'SVANTEK' Integrating Sound Level Meter  
 Manufacturer : SVANTEK  
 Model No. : SVAN 957  
 Serial No. : 21460  
 Microphone No. : 43679  
 Equipment No. : N-08-09

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
 Relative Humidity : 40-70%

**Test Specifications**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Reading, dB
94	94.0
114	114.0

\*\*\*\*\*

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
 General Manager

### TEST REPORT

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34872
Date of Issue:	2021-03-08
Date Received:	2021-03-05
Date Tested:	2021-03-05
Date Completed:	2021-03-08
Next Due Date:	2022-03-07

Page: 1 of 1

**ATTN:** Mr. W. K. Tang

### Certificate of Calibration

**Item for calibration:**

Description : Sound Level Meter  
Manufacturer : BSWA  
Model No. : BSWA 308  
Serial No. : 570271  
Equipment No. : WN-01-01

**Test conditions:**

Room Temperature : 17-22 degree Celsius  
Relative Humidity : 40-70%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34872F
Date of Issue:	2021-03-08
Date Received:	2021-03-05
Date Tested:	2021-03-05
Date Completed:	2021-03-08
Next Due Date:	2022-03-07

Page: 1 of 1

**ATTN:** Mr. W. K. Tang

**Certificate of Calibration**

**Item for calibration:**

Description : Sound Level Meter  
Manufacturer : BSWA  
Model No. : BSWA 308  
Serial No. : 580014  
Equipment No. : WN-01-07

**Test conditions:**

Room Temperature : 17-22 degree Celsius  
Relative Humidity : 40-70%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*  
For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	33963
Date of Issue:	2020-08-21
Date Received:	2020-08-19
Date Tested:	2020-08-19
Date Completed:	2020-08-21
Next Due Date:	2021-08-20
Page:	1 of 1

**ATTN:** Mr. W. K. Tang

**Certificate of Calibration**

**Item for Calibration:**

Description : Acoustical Calibrator  
 Manufacturer : Brüel & Kjær  
 Model No. : 4231  
 Serial No. : 2412367  
 Equipment No. : N-02-03

**Test Conditions:**

Room Temperature : 17-22 degree Celsius  
 Relative Humidity : 40-70%

**Methodology:**

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1dB
At 114 dB SPL	114.0	114.0 ± 0.1dB

Remark: This report supersedes the one dated 2019-08-20 with certificate number 31951.

\*\*\*\*\*

*PREPARED AND CHECKED BY:*  
 For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
 General Manager

### TEST REPORT

APPLICANT: Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	33963A
Date of Issue:	2020-08-21
Date Received:	2020-08-19
Date Tested:	2020-08-19
Date Completed:	2020-08-21
Next Due Date:	2021-08-20

Page: 1 of 1

ATTN: Mr. W. K. Tang

### Certificate of Calibration

**Item for calibration:**

Description : Acoustical Calibrator  
Manufacturer : SVANTEK  
Model No. : SV30A  
Serial No. : 24791  
Equipment No. : N-09-04

**Test conditions:**

Room Temperature : 17-22 degree Celsius  
Relative Humidity : 40-70%

**Methodology:**

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**

  
PATRICK TSE  
General Manager

**TEST REPORT**

**APPLICANT:** Wellab Limited  
(EM&A Department)  
Room 1701, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	34136A
Date of Issue:	2020-10-03
Date Received:	2020-09-29
Date Tested:	2020-09-29
Date Completed:	2020-10-03
Next Due Date:	2021-10-02

Page: 1 of 1

**ATTN:** Mr. W. K. Tang

**Certificate of Calibration**

**Item for calibration:**

Description : Acoustical Calibrator  
Manufacturer : SVANTEK  
Model No. : SV30A  
Serial No. : 24780  
Equipment No. : N-09-05

**Test conditions:**

Room Temperature : 17-22 degree Celsius  
Relative Humidity : 40-70%

**Methodology:**

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

**Results:**

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
General Manager

---

---

**APPENDIX C  
ENVIRONMENTAL MONITORING  
SCHEDULES**

---

---

**DC/2009/10, HATS 2A Upgrading Main Pumping Station, Sedimentation Tanks and Ancillary Facilities at SCISTW  
Impact Air Quality and Noise Monitoring Schedule (April 2021)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-Apr	2-Apr	3-Apr
				1hr TSP X 3 Noise 24 hr TSP		
4-Apr	5-Apr	6-Apr	7-Apr	8-Apr	9-Apr	10-Apr
			1hr TSP X 3 Noise 24 hr TSP			
11-Apr	12-Apr	13-Apr	14-Apr	15-Apr	16-Apr	17-Apr
	24 hr TSP	1hr TSP X 3 Noise			24 hr TSP	
18-Apr	19-Apr	20-Apr	21-Apr	22-Apr	23-Apr	24-Apr
	1hr TSP X 3 Noise			24 hr TSP	1hr TSP X 3	
25-Apr	26-Apr	27-Apr	28-Apr	29-Apr	30-Apr	
			24 hr TSP	1hr TSP X 3 Noise		

**Air Quality Monitoring Station**

AM7 - West Kowloon No.2 Sewage Pumping Station  
AM8 - Block A of Government Dockyard  
AM6b - Works Site Boundary

**Noise Monitoring Station**

NM6 - Customs' Marine Base (Block H of Government Dockyard) Rooftop  
NM5 - FSD Diving Training Centre



**DC/2009/10, HATS 2A Upgrading Main Pumping Station, Sedimentation Tanks and Ancillary Facilities at SCISTW  
Tentative Impact Air Quality and Noise Monitoring Schedule (May 2021)**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						<b>1-May</b>
<b>2-May</b>	3-May	4-May	5-May	6-May	7-May	8-May
		24 hr TSP	1hr TSP X 3 Noise			
<b>9-May</b>	10-May	11-May	12-May	13-May	14-May	15-May
	24 hr TSP	1hr TSP X 3 Noise			24 hr TSP	
<b>16-May</b>	17-May	18-May	<b>19-May</b>	20-May	21-May	22-May
	1hr TSP X 3 Noise			24 hr TSP	1hr TSP X 3	
<b>23-May</b>	24-May	25-May	26-May	27-May	28-May	29-May
			24 hr TSP	1hr TSP X 3 Noise		
<b>30-May</b>	31-May					

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Air Quality Monitoring Station**

AM7 - West Kowloon No.2 Sewage Pumping Station  
AM8 - Block A of Government Dockyard  
AM6b - Works Site Boundary

**Noise Monitoring Station**

NM6 - Customs' Marine Base (Block H of Government Dockyard) Rooftop  
NM5 - FSD Diving Training Centre

---

**APPENDIX D  
1-HOUR AND 24-HOUR TSP  
MONITORING RESULTS AND  
GRAPHICAL PRESENTATION**

---

## Appendix D - 1-hour TSP Monitoring Results

### Location AM6b - Works Site Boundary

Start Date	Start Time	Weather Condition	Air Temp. (K)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )	Filter ID no.
				Initial	Final		Initial	Final		Initial	Final				
1-Apr-21	9:00	Cloudy	299.9	3.4882	3.5018	0.0136	11666.8	11667.8	1.0	1.20	1.19	1.19	71.7	189.8	210401/013
1-Apr-21	10:00	Cloudy	300.8	3.4799	3.4937	0.0138	11667.8	11668.8	1.0	1.19	1.19	1.19	71.6	192.8	210401/014
1-Apr-21	11:00	Cloudy	301.1	3.4993	3.5155	0.0162	11668.8	11669.8	1.0	1.19	1.19	1.19	71.5	226.5	210401/018
7-Apr-21	9:00	Cloudy	296.3	3.5120	3.5311	0.0191	11693.8	11694.8	1.0	1.21	1.20	1.21	72.4	263.7	210401/020
7-Apr-21	10:00	Cloudy	295.0	3.5049	3.5203	0.0154	11694.8	11695.8	1.0	1.21	1.21	1.21	72.6	212.1	210401/021
7-Apr-21	11:00	Cloudy	295.3	3.5012	3.5149	0.0137	11695.8	11696.8	1.0	1.21	1.21	1.21	72.6	188.8	210401/022
13-Apr-21	9:00	Sunny	299.3	3.3100	3.3176	0.0076	11744.8	11745.8	1.0	1.22	1.22	1.22	73.2	103.8	210301/079
13-Apr-21	10:00	Sunny	299.7	3.2154	3.2247	0.0093	11745.8	11746.8	1.0	1.22	1.22	1.22	73.2	127.1	210301/080
13-Apr-21	11:00	Sunny	300.4	3.4656	3.4797	0.0141	11746.8	11747.8	1.0	1.22	1.22	1.22	73.1	193.0	210401/017
19-Apr-21	9:00	Cloudy	294.6	3.4575	3.4792	0.0217	11771.8	11772.8	1.0	1.23	1.23	1.23	73.8	294.1	210401/067
19-Apr-21	10:00	Cloudy	295.1	3.4789	3.4997	0.0208	11772.8	11773.8	1.0	1.23	1.23	1.23	73.7	282.2	210401/068
19-Apr-21	11:00	Cloudy	295.9	3.4951	3.5154	0.0203	11773.8	11774.8	1.0	1.23	1.22	1.23	73.6	275.8	210401/069
23-Apr-21	9:00	Sunny	299.6	3.4875	3.5076	0.0201	11798.8	11799.8	1.0	1.22	1.22	1.22	73.0	275.4	210401/090
23-Apr-21	10:00	Sunny	300.9	3.4865	3.5052	0.0187	11799.8	11800.8	1.0	1.22	1.21	1.21	72.8	256.9	210401/089
23-Apr-21	11:00	Sunny	301.9	3.5014	3.5227	0.0213	11800.8	11801.8	1.0	1.21	1.21	1.21	72.7	293.2	210401/088
29-Apr-21	9:00	Cloudy	295.5	3.5036	3.5102	0.0066	11825.8	11826.8	1.0	1.23	1.23	1.23	73.7	89.6	210501/012
29-Apr-21	10:00	Cloudy	296.5	3.5232	3.5291	0.0059	11826.8	11827.8	1.0	1.23	1.22	1.23	73.6	80.2	210501/013
29-Apr-21	11:00	Cloudy	297.5	3.5166	3.5235	0.0069	11827.8	11828.8	1.0	1.22	1.22	1.22	73.4	94.0	210501/013
													Min	80	
													Max	294	
													Average	202	

## Appendix D - 1-hour TSP Monitoring Results

Location AM7 - North West Kowloon Sewage Pumping Station			
Date	Time	Weather	Particulate Concentration ( $\mu\text{g}/\text{m}^3$ )
1-Apr-21	9:00	Fine	82.0
1-Apr-21	10:00	Fine	99.2
1-Apr-21	11:00	Fine	94.0
7-Apr-21	9:00	Cloudy	142.6
7-Apr-21	10:00	Cloudy	134.0
7-Apr-21	11:00	Cloudy	137.6
13-Apr-21	9:00	Sunny	55.8
13-Apr-21	10:00	Sunny	59.6
13-Apr-21	11:00	Sunny	65.7
19-Apr-21	9:00	Cloudy	144.4
19-Apr-21	10:00	Cloudy	135.2
19-Apr-21	11:00	Cloudy	141.6
23-Apr-21	9:00	Sunny	162.2
23-Apr-21	10:00	Sunny	130.9
23-Apr-21	11:00	Sunny	129.6
29-Apr-21	9:00	Cloudy	92.3
29-Apr-21	10:00	Cloudy	78.4
29-Apr-21	11:00	Cloudy	55.5
		Minimum	55.5
		Maximum	162.2
		Average	107.8

Location AM8 - Block A of Government Dockyard			
Date	Time	Weather	Particulate Concentration ( $\mu\text{g}/\text{m}^3$ )
1-Apr-21	8:40	Fine	71.6
1-Apr-21	9:40	Fine	86.7
1-Apr-21	10:40	Fine	81.3
7-Apr-21	13:00	Sunny	109.4
7-Apr-21	14:00	Sunny	123.1
7-Apr-21	15:00	Sunny	115.7
13-Apr-21	13:00	Sunny	45.7
13-Apr-21	14:00	Sunny	47.7
13-Apr-21	15:00	Sunny	52.1
19-Apr-21	13:00	Cloudy	119.5
19-Apr-21	14:00	Cloudy	125.4
19-Apr-21	15:00	Cloudy	117.1
23-Apr-21	13:00	Sunny	98.0
23-Apr-21	14:00	Sunny	92.6
23-Apr-21	15:00	Sunny	86.5
29-Apr-21	13:00	Cloudy	49.5
29-Apr-21	14:00	Cloudy	56.9
29-Apr-21	15:00	Cloudy	81.4
		Minimum	45.7
		Maximum	125.4
		Average	86.7

## Appendix D - 24-hour TSP Monitoring Results

### Location AM6b - Works Site Boundary

Start Date	Weather Condition	Air Temp. (K)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )	Filter ID no.
			Initial	Final		Initial	Final		Initial	Final				
1-Apr-21	Cloudy	301.5	3.3246	3.4969	0.1723	11669.8	11693.8	24.0	1.19	1.20	1.19	1719.6	100.2	210301/077
7-Apr-21	Cloudy	296.9	3.4952	3.6234	0.1282	11696.8	11720.8	24.0	1.20	1.20	1.20	1734.4	73.9	210401/023
12-Apr-21	Cloudy	297.7	3.5133	3.6277	0.1144	11720.8	11744.8	24.0	1.23	1.22	1.22	1763.6	64.9	210401/027
16-Apr-21	Cloudy	294.9	3.4501	3.4987	0.0486	11747.8	11771.8	24.0	1.23	1.23	1.23	1771.1	27.4	210401/060
22-Apr-21	Sunny	298.2	3.5138	3.7014	0.1876	11774.8	11798.8	24.0	1.22	1.22	1.22	1756.9	106.8	210401/070
28-Apr-21	Cloudy	295.8	3.4495	3.5629	0.1134	11801.8	11825.8	24.0	1.23	1.23	1.23	1767.9	64.1	210401/086
												Min	27	
												Max	107	
												Average	73	




### Location AM7 - North West Kowloon Sewage Pumping Station


Start Date	Weather Condition	Air Temp. (K)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )	Filter ID no.
			Initial	Final		Initial	Final		Initial	Final				
1-Apr-21	Cloudy	301.1	3.2667	3.3709	0.1042	40878.4	40902.4	24.0	1.19	1.19	1.19	1715.8	60.7	210301/076
7-Apr-21	Cloudy	295.7	3.5112	3.5986	0.0874	40902.4	40926.4	24.0	1.21	1.20	1.21	1738.0	50.3	210401/025
12-Apr-21	Cloudy	297.7	3.4801	3.5539	0.0738	40926.4	40950.4	24.0	1.22	1.21	1.21	1744.0	42.3	210401/028
16-Apr-21	Cloudy	294.9	3.5031	3.5936	0.0905	40950.4	40974.4	24.0	1.22	1.22	1.22	1751.6	51.7	210401/059
22-Apr-21	Sunny	298.2	3.4758	3.6126	0.1368	40974.4	40998.4	24.0	1.21	1.20	1.21	1737.1	78.8	210401/071
28-Apr-21	Cloudy	295.8	3.4997	3.5949	0.0952	40998.4	41022.4	24.0	1.21	1.22	1.21	1748.3	54.5	210401/087
												Min	42	
												Max	79	
												Average	56	

### Location AM8 - Block A of Government Dockyard




Start Date	Weather Condition	Air Temp. (K)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m <sup>3</sup> /min.)		Av. flow (m <sup>3</sup> /min)	Total vol. (m <sup>3</sup> )	Conc. (µg/m <sup>3</sup> )	Filter ID no.
			Initial	Final		Initial	Final		Initial	Final				
1-Apr-21	Cloudy	301.1	3.2648	3.4011	0.1363	13812.2	13836.2	24.0	1.19	1.19	1.19	1719.1	79.3	210301/078
7-Apr-21	Cloudy	296.9	3.5178	3.6097	0.0919	13836.2	13860.2	24.0	1.21	1.21	1.21	1736.4	52.9	210401/024
12-Apr-21	Cloudy	297.7	3.4632	3.5525	0.0893	13860.2	13884.2	24.0	1.21	1.21	1.21	1742.8	51.2	210401/029
16-Apr-21	Cloudy	294.9	3.4577	3.5640	0.1063	13884.2	13908.2	24.0	1.21	1.22	1.22	1750.1	60.7	210401/061
22-Apr-21	Sunny	298.2	3.4971	3.6300	0.1329	13908.2	13932.2	24.0	1.21	1.20	1.21	1736.3	76.5	210401/072
28-Apr-21	Cloudy	295.8	3.4586	3.5402	0.0816	13932.2	13956.2	24.0	1.21	1.21	1.21	1747.0	46.7	210401/085
												Min	47	
												Max	79	
												Average	61	

### 1-hr TSP Concentration Levels

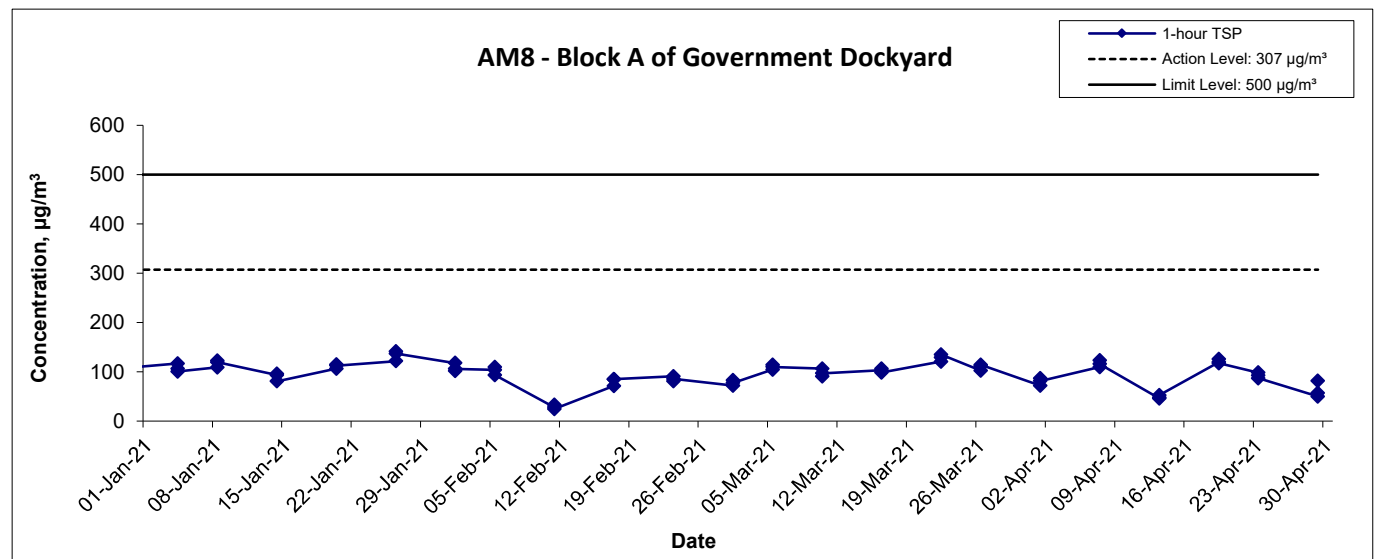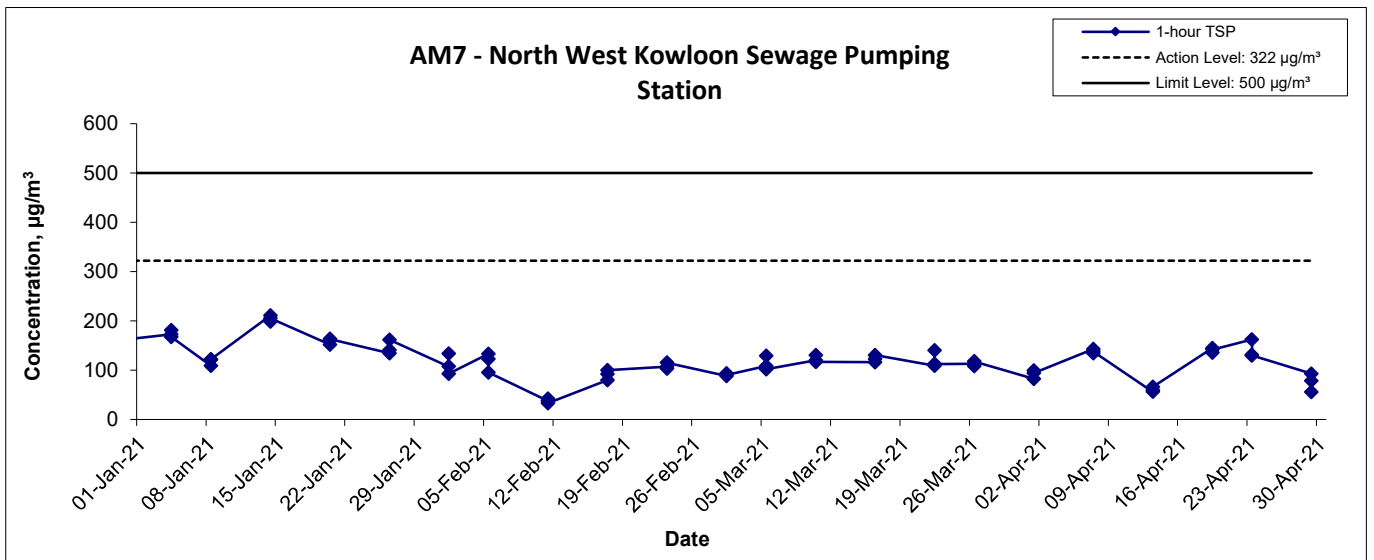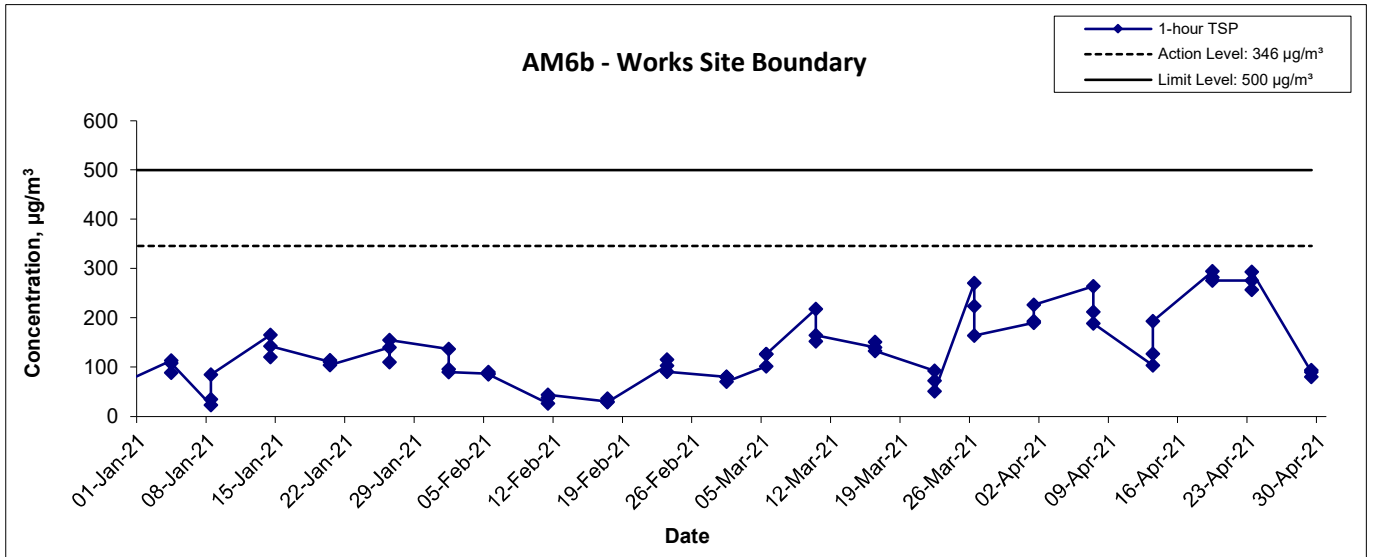

Title Contract No. DC/2009/10 HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary Graphical Presentation of 1-hour TSP Monitoring Results	Scale N.T.S	Project No. MA11007	 consulting . testing . research
	Date Apr 21	Appendix D	

### 24-hr TSP Concentration Levels

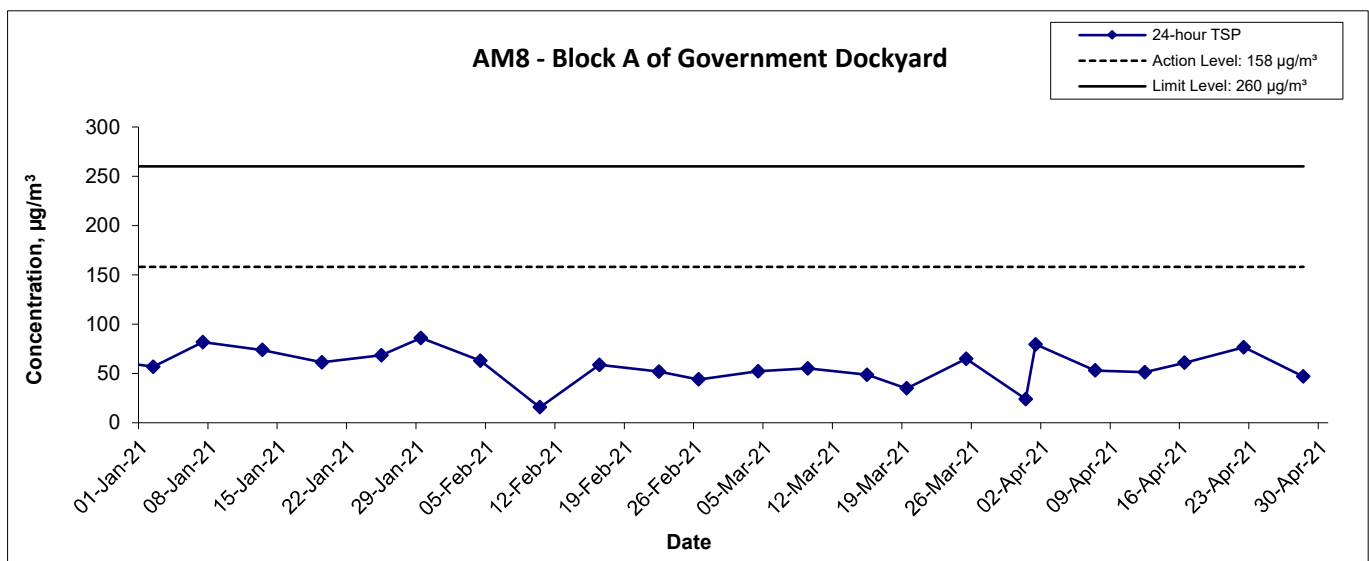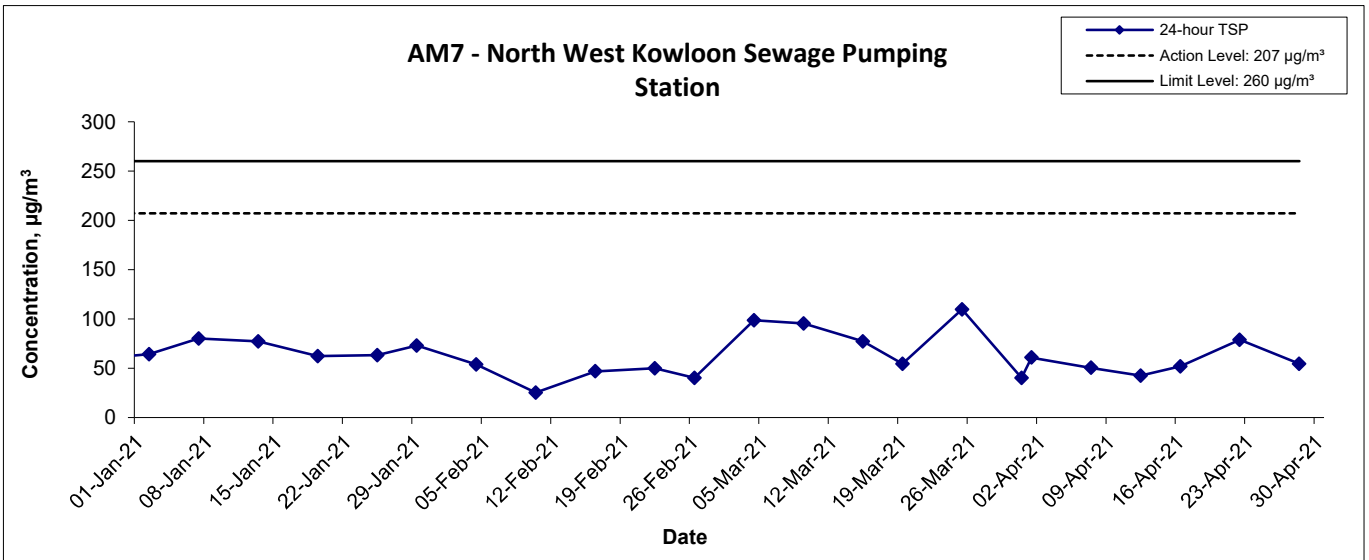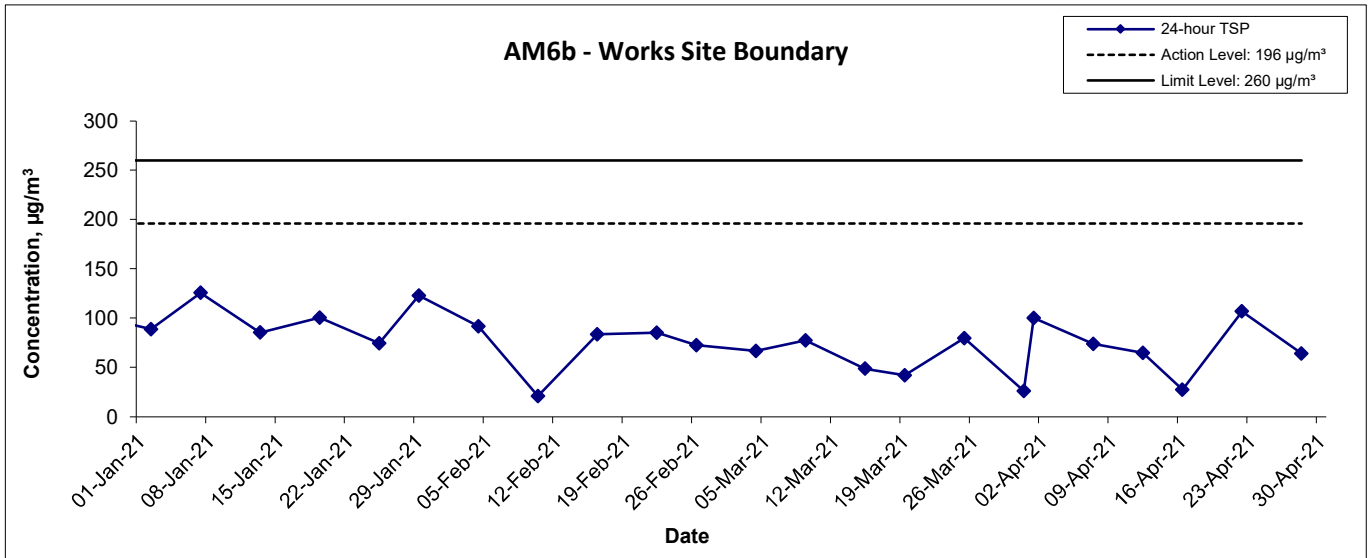

Title Contract No. DC/2009/10 HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary Graphical Presentation of 24-hour TSP Monitoring Results	Scale N.T.S	Project No. MA11007	
	Date Apr 21	Appendix D	

---

---

**APPENDIX E  
NOISE MONITORING RESULTS AND  
GRAPHICAL PRESENTATIONS**

---

---



## Appendix E - Noise Monitoring Results



(0700-1900 hrs on Normal Weekdays)

<b>Location NM5 - Near FSD Diving Rescue and Training Centre</b>					
Date	Time	Weather	Unit: dB (A) (30-min)		
			Measured Noise Level		
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>
1-Apr-21	09:20	Cloudy	58.2	61.3	48.5
7-Apr-21	10:05	Cloudy	61.2	63.7	58.2
13-Apr-21	09:40	Sunny	66.0	68.7	60.5
19-Apr-21	10:30	Cloudy	60.1	63.4	56.9
29-Apr-21	08:20	Cloudy	61.0	64.0	57.5
		Maximum	66.0		
		Minimum	58.2		

<b>Location NM6 - Customs' Marine Base (Block H of Government Dockyard) Rooftop</b>					
Date	Time	Weather	Unit: dB (A) (30-min)		
			Measured Noise Level		
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>
1-Apr-21	11:20	Cloudy	69.3	61.9	51.6
7-Apr-21	13:35	Sunny	60.9	61.3	58.4
13-Apr-21	13:20	Sunny	65.3	66.8	58.7
19-Apr-21	13:35	Cloudy	57.9	59.7	55.2
29-Apr-21	14:30	Cloudy	56.3	57.5	55.0
		Maximum	69.3		
		Minimum	56.3		

## Noise Levels

(0700-1900 hrs on Normal Weekdays)

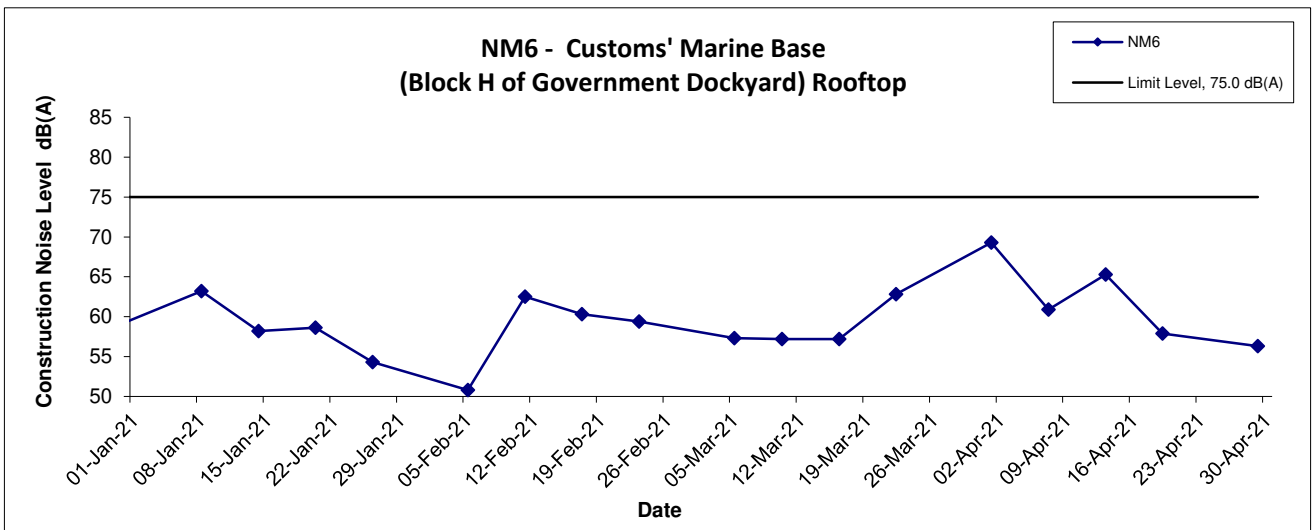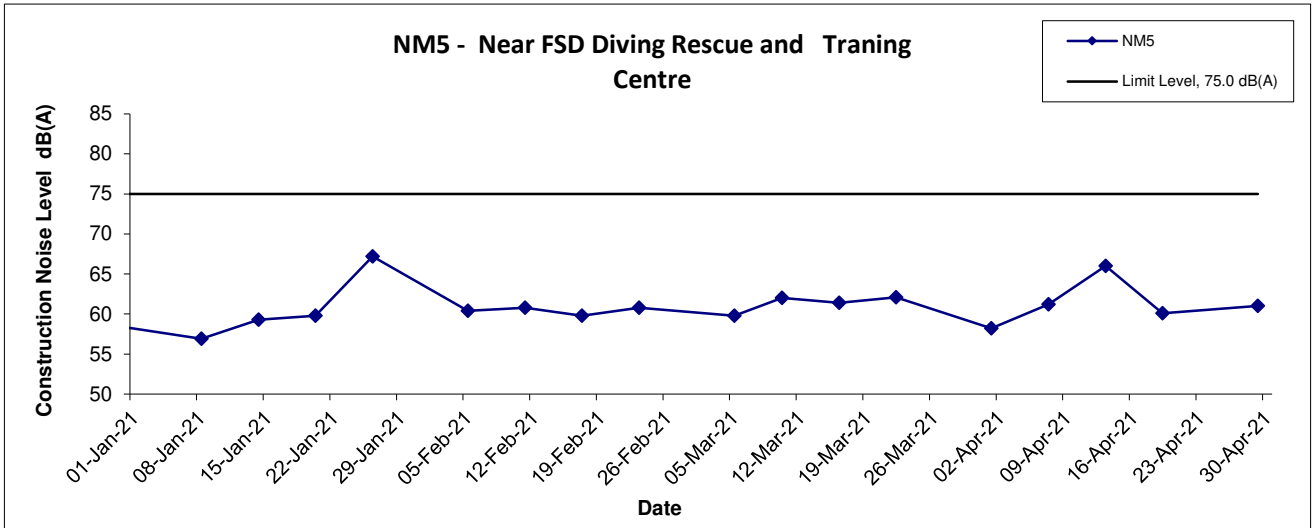

Title Contract No. DC/2009/10 HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary  Graphical Presentation of Noise Monitoring Result	Scale N.T.S	Project No. MA11007	 consulting . testing . research
	Date Apr 21	Appendix E	

---

---

**APPENDIX F**  
**SUMMARY OF EXCEEDANCE**

---

---

## **APPENDIX F – SUMMARY OF EXCEEDANCE**

**Reporting Month:** April 2021

- a) Exceedance Report for 1-hr TSP (NIL)**
- b) Exceedance Report for 24-hr TSP (NIL)**
- c) Exceedance Report for Construction Noise (NIL)**

---

---

**APPENDIX G  
SITE AUDIT SUMMARY**

---

---

Contract No: DC/2009/10

**HATS 2A Upgrading Main Pumping Station,  
Sedimentation Tanks and Ancillary Facilities at SCISTW**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	210401
Date	1 April 2021 (Thursday)
Time	9:30 – 10:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part A – Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part B – Landscape and Visual</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part C – Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D – Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E – Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F – Permit / Licence</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Remark:</b></p> <ul style="list-style-type: none"><li>• Follow-up on previous audit sessions: On previous audit session (Ref. No. 210325), no environmental deficiency was observed during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Jack Cheung		7 April 2021
Checked by	Dr. Priscilla Choy		7 April 2021

Contract No: DC/2009/10

**HATS 2A Upgrading Main Pumping Station,  
Sedimentation Tanks and Ancillary Facilities at SCISTW**



**Record Summary of Environmental Site Inspection**

**Inspection Information**

Checklist Reference Number	210408
Date	8 April 2021 (Thursday)
Time	9:30 – 10:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part A - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part B - Landscape and Visual</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part C - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Permit / Licence</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Remark:</b></p> <ul style="list-style-type: none"><li>• Follow-up on previous audit sessions: On previous audit session (Ref. No. 210401), no environmental deficiency was observed during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Jack Cheung		12 April 2021
Checked by	Dr. Priscilla Choy		12 April 2021

Contract No: DC/2009/10

HATS 2A Upgrading Main Pumping Station,

Sedimentation Tanks and Ancillary Facilities at SCISTW

Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	210414
Date	14 April 2021 (Wednesday)
Time	14:00 – 14:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part A - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part B - Landscape and Visual</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part C - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Permit / Licence</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Remark:</b></p> <ul style="list-style-type: none"><li>• Follow-up on previous audit sessions: On previous audit session (Ref. No. 210408), no environmental deficiency was observed during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Ivan Wong		16 April 2021
Checked by	Dr. Priscilla Choy		16 April 2021



Contract No: DC/2009/10

HATS 2A Upgrading Main Pumping Station,

Sedimentation Tanks and Ancillary Facilities at SCISTW

Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	210422
Date	22 April 2021 (Thursday)
Time	09:30 – 10:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part A - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part B - Landscape and Visual</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part C - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Permit / Licence</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Remark:</b></p> <ul style="list-style-type: none"><li>• Follow-up on previous audit sessions: On previous audit session (Ref. No. 210414), no environmental deficiency was observed during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Ivan Wong		26 April 2021
Checked by	Dr. Priscilla Choy		26 April 2021

Contract No: DC/2009/10

HATS 2A Upgrading Main Pumping Station,

Sedimentation Tanks and Ancillary Facilities at SCISTW



Record Summary of Environmental Site Inspection

Inspection Information

Checklist Reference Number	210429
Date	29 April 2021 (Thursday)
Time	09:30 – 10:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>Part A - Water Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part B - Landscape and Visual</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part C - Air Quality</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part D - Noise</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part E - Waste / Chemical Management</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Part F - Permit / Licence</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Others</b></p> <ul style="list-style-type: none"><li>• No environmental deficiency was identified during the site inspection.</li></ul> <p><b>Remark:</b></p> <ul style="list-style-type: none"><li>• Follow-up on previous audit sessions: On previous audit session (Ref. No. 210422), no environmental deficiency was observed during site inspection.</li></ul>	

	Name	Signature	Date
Recorded by	Ivan Wong		3 May 2021
Checked by	Dr. Priscilla Choy		3 May 2021

---

---

**APPENDIX H  
SUMMARY OF AMOUNT OF WASTE  
GENERATED**

---

---

Name of Department:                     DSD                    

Contract No. :                     DC/2009/10                    

**Monthly Summary Waste Flow Table for 2021 (year)**

Month	Actual Quantities of inert C&D Materials Generated Monthly						Actual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard	Plastics (see Note 3)	Chemical Waste	Other, e.g. general refuse
	(In '000m <sup>3</sup> )	(In '000m <sup>3</sup> )	(In '000m <sup>3</sup> )	(In '000m <sup>3</sup> )	(In '000m <sup>3</sup> )	(In '000m <sup>3</sup> )	(In '000kg)	(In '000kg)	(In '000kg)	(In '000kg)	(In '000m <sup>3</sup> )
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.002
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.003
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May											
June											
Sub-total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.004
July											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.004
Total since commence ment of project	61.956	61.952	0.000	0.000	61.956	0.000	372.871	11.905	3.314	2.227	2.128

Notes:

- (1) The performance targets are given in PS Clause 25.41(14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
- (4) The conversion factor for tonne to m<sup>3</sup> for inert C&D materials is 1.9 tonne/m<sup>3</sup>.
- (5) The conversion factor for tonne to m<sup>3</sup> for general refuse is 1.8 tonne/m<sup>3</sup>.

---

---

**APPENDIX I**  
**EVENT ACTION PLANS**

---

---

## APPENDIX I – Event / Action Plans

**Table I-1 Event / Action Plan For Air Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b>LIMIT LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented;	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	<p>implemented;</p> <p>6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</p> <p>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring</p>	<p>advise the ER accordingly;</p> <p>5. Supervise the implementation of remedial measures.</p>	<p>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</p>	<p>control;</p> <p>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated</p>



**Table I-2 Event / Action Plan For Construction Noise**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol style="list-style-type: none"> <li>1. Notify ER, IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the IEC and Contractor on remedial measures required;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the investigation results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Advise the ER on the effectiveness of the proposed remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC and ER;</li> <li>2. Implement noise mitigation proposals</li> </ol>
Limit Level being exceeded	<ol style="list-style-type: none"> <li>1. Inform IEC, ER, Contractor and EPD;</li> <li>2. Repeat measurements to confirm findings;</li> <li>3. Increase monitoring frequency;</li> <li>4. Identify source and investigate the cause of exceedance;</li> <li>5. Carry out analysis of Contractor's working procedures;</li> <li>6. Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Submit further proposal if problem still not under control;</li> <li>5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated</li> </ol>

---

---

**APPENDIX J  
ENVIRONMENTAL MITIGATION  
IMPLEMENTATION SCHEDULE (EMIS)**

---

---

**-APPENDIX J IMPLEMENTATION SCHEDULE OF ENVIRONMENTAL MITIGATION MEASURES (EMIS)**

<b>EIA Ref.</b>	<b>Recommended Mitigation Measures</b>	<b>Location of the measure</b>	<b>Implementation Status</b>
<b>A</b>	<b>Air Quality</b>		
3.74	Skip hoist for material transport should be totally enclosed by impervious sheeting.	All construction sites	^
	Vehicle washing facilities should be provided at every vehicle exit point.		^
	The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcore.		^
	Where a site boundary adjoins a road, streets or other areas accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit.		N/A
	Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.		^
	Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.		^
	Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.		^
	Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.		^
	Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit.		^
	Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides.		^
	Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.		^
3.74	Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.	All construction sites	^

<b>EIA Ref.</b>	<b>Recommended Mitigation Measures</b>	<b>Location of the measure</b>	<b>Implementation Status</b>
<b>B</b>	<b>Airborne Noise</b>		
4.56– 4.61	Use of quiet PME, movable barriers and acoustic mats.	All construction sites	^
4.67	Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program.		^
	Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program.		^
	Mobile plant, if any, shall be sited as far away from NSRs as possible.		^
	Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum.		^
4.67	Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.		^
	Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities.		^
<b>C</b>	<b>Water Quality</b>		
6.349 to 6.375	Construction Site Runoff and General Construction Activities The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.	All construction sites	^
6.376	Effluent Discharge There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.		^
6.377	Accidental Spillage of Chemicals  Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General)		^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
	Regulation should be observed and complied with for control of chemical wastes.		
6.378	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.		^
6.379	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>		^
6.380	<p>Construction Works in Close Proximity of Storm Drains or Seafront:</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea.</li> </ul>	All construction sites	^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
<b>D</b>	<b>Waste Management</b>		
9.107	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimize wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All construction sites	^
9.109	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All construction sites	^
9.113	Sort C&D waste from demolition of existing facilities to recover recyclable portions such as metals.		^
	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.		^
	Encourage collection of aluminum cans, PET bottles and paper by providing separate labeled bins to enable these wastes to be segregated from other general refuse generated by the work force.		^
	Any unused chemicals or those with remaining functional capacity shall be recycled.		^
	Proper storage and site practices to minimize the potential for damage or contamination of construction materials.		^
9.115	Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.		^
	Training of site personnel in proper waste management and chemical waste handling procedures.		^
9.115	Develop and provide toolbox talk for on-site sorting of C&D materials to enhance worker's awareness in handling, sorting, reuse and recycling of C&D materials.		^
	Provision of sufficient waste disposal points and regular collection of waste.		^
	Regular cleaning and maintenance programme for drainage systems, sumps and oil		^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
	interceptors.		
9.125	Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage”.	All construction sites	^
9.131	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.		^
9.133	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.		^
9.135	The recyclable component of the municipal waste generated by the workforce, such as aluminum cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.		^
9.137	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.		^
9.142	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.		N/A

<b>EIA Ref.</b>	<b>Recommended Mitigation Measures</b>	<b>Location of the measure</b>	<b>Implementation Status</b>
<b>E Terrestrial Ecology</b>			
10.94	To implement effective noise mitigation measures as recommended in Section 4 of EIA.	All construction sites	N/A
10.95	Dust control practices such as regular watering, complete coverage of any aggregate or dusty material storage piles, and re-schedule of dusty activities during high-wind conditions as well as other measures recommended in Section 3 of EIA, should be implemented.		^
10.96	Fences/hoardings should be erected and installed along the boundary of the works areas.		^
10.97	Standard good site practices as suggested in Section 10 of EIA should be implemented.		N/A
10.98	Provision of proper drainage system and runoff control measures such as use of sand/silt traps, oil/grease separators, sedimentation tanks, etc.		^
<b>F Landscape and Visual</b>			
Table 13.7	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	All construction sites	^
	Existing trees to be retained on site should be carefully protected during construction.		^
	Trees unavoidably affected by the works should be transplanted where practical.		^
	Compensatory tree planting should be provided to compensate for felled trees.		^
	Control of night-time lighting.		^
Table 13.7	Erection of decorative screen hoarding compatible with the surrounding setting.	All construction sites	N/A
<b>G Marine Ecology</b>			
11.137	To minimize the potential indirect impacts on water quality from construction site runoff and various construction activities, the practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted.	All construction sites	^
<b>H Hazard to Life</b>			
14A.201	Limiting use of cranes in terms of locations, lifting height, swing angle and setting up safety zone.	Exact location will be determined on construction site by the engineer	^



Remarks:	^ Compliance of mitigation measure;
	N/A Not Applicable;
	* Recommendation was made during site audit but improved/rectified by the contractor.
	# Recommendation was made during site audit and to be improved / rectified by the contractor.
	X Non-compliance of mitigation measure;
	• Non-compliance but rectified by the contractor;

---

---

**APPENDIX K  
COMPLAINT LOG**

---

---

**APPENDIX K – COMPLAINT LOG**

**Reporting Month:** April 2021

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
N.A.	N.A.	N.A.	N.A.	N.A.	N.A.

**Remarks:** No environmental complaint was received in the reporting month.



---

---

**APPENDIX L**  
**CONSTRUCTION PROGRAMME**

---

---

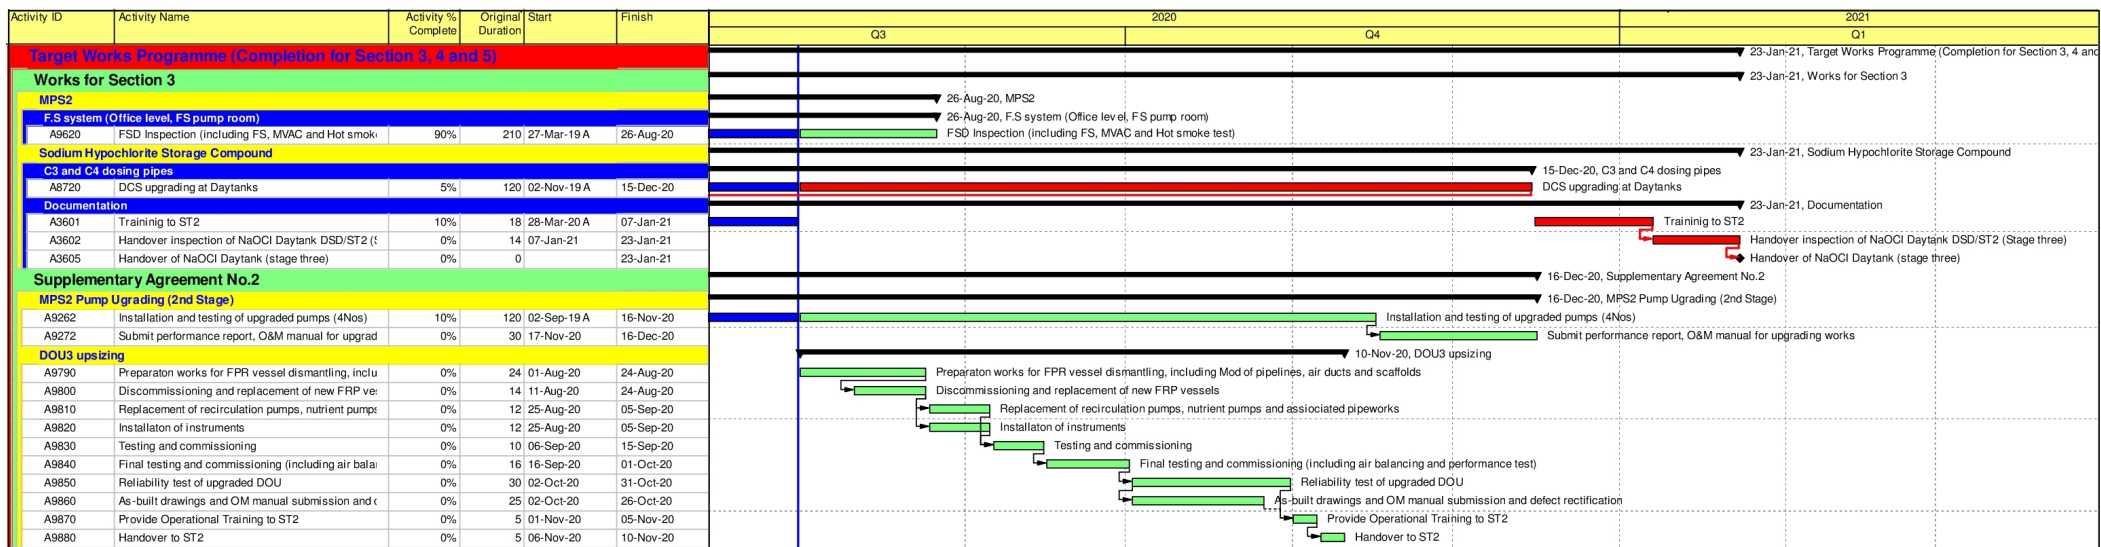

Contract No. DC/2009/10

HATS Stage 2A - Upgrading works at StoneCutters Island Sewage Treatment Works

Target Works Programme for Completion of Section 3, 4 and 5

Date	Revision	Checked	Approved
26-Jul-18	Rev. 5		
20-Nov-18	Rev. 6		
11-Feb-19	Rev. 7		
