



# Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong

2<sup>nd</sup> Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

20 April 2021

Project No.: 0540005



Document details	
Document title	Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong
Document subtitle	2 <sup>nd</sup> Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)
Project No.	0540005
Date	20 April 2021
√ersion	2.0
Author	Susan Chan
Client Name	Ocean Park Corporation

				ERM approva		
Version	Revision	Author	Reviewed by	Name	Date	Comments
Draft	1.0	Susan Chan	Mandy To	Terence Fong	19.4.2021	-
Revised	2.0	Susan Chan	Mandy To	Terence Fong	20.4.2021	IEC

Document history





## Environmental Permit No. EP-249/2006/D

## Ocean Park Master Redevelopment Project

#### **Environmental Team Leader Certification**

#### Reference Document/Plan

Document/Plan to be Certified/ Verified: Monthly EM&A Report (6 Mar to 5 Apr 2021)

Date of Report: 20 April 2020

#### **Reference EP Condition**

Environmental Permit Condition: 3.4

Four hard copies and one electronic copy of the monthly EM&A Reports for the construction and operation stages shall be submitted to the Director within two weeks after the end of the reporting month. The monthly EM&A Reports shall include a summary of all non-compliance with the recommendations in the EIA Report or this Permit. The submissions shall be certified by the ET Leader and verified by the IEC as complied with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided upon request by the Director.

#### **ETL Verification**

I hereby verify that the above referenced document/<del>plan</del> complies with the above referenced condition of EP-249/2006/D.

Ms Mandy To

Date: 20 April 2020

Environmental Team Leader

Alandy 20.

Our ref: 0540005\_ETL Verification Cert\_2\_20200420.docx



Ocean Park Corporation 180 Wong Chuk Hang Road Aberdeen Hong Kong

Attn: Ms. Eva Au Yeung

Our Reference AFK/EC/hI/416500/02.02/ L-0006

3/F International Trade Tower 348 Kwun Tong Road Kowloon Hong Kong

T +852 2828 5757 F +852 2827 1823 mottmac.hk Ocean Park Master Redevelopment Project Contract No. P007
Independent Environmental Checker (IEC)
Environmental Permit No. EP-249/2006/D - Condition 3.1
Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong – 2<sup>nd</sup> Monthly Noise Monitoring Report dated 20 April 2021

20 April 2021 By Email and Post

Dear Eva,

I refer to the captioned submission dated 20 April 2021 which has been revised as per our comments dated 20 April 2021. Pursuant to the requirement under Condition 3.1 of the Environmental Permit No. EP-249/2006/D, I hereby verify the Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong –  $2^{nd}$  Monthly Noise Monitoring Report for the Project.

Yours sincerely, for MOTT MACDONALD HONG KONG LIMITED

Ir Eric Ching

Independent Environmental Checker (IEC)

T 2828 5825

Eric.Ching@mottmac.com

## Ocean Park Master Redevelopment Project

Environmental Permit No. EP-249/2006/D - Condition 3.1

Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong

2<sup>nd</sup> Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

Submitted by ERM-Hong Kong, Limited dated 20-04-2021

This is to verify that

Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong 2<sup>nd</sup> Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

Submitted by ERM-Hong Kong, Limited

dated 20-04-2021

Has been verified by the undersigned.

Signed

Ir Eric Ching

Independent Environmental Checker (IEC) Retained by Ocean Park Corporation

pursuant to Environmental Permit No. EP-249/2006/D

Date

20 April 2021

#### **Signature Page**

20 April 2021

## **Update of Design of the Existing Lagoon Show in Ocean Park Hong Kong**

2nd Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

Terence Fong Partner

ERM-Hong Kong, Limited 2509, 25/F One Harbourfront, 18 Tak Fung Street, Hunghom, Kowloon Hong Kong

© Copyright 2021 by ERM Worldwide Group Ltd and/or its affiliates ("ERM"). All rights reserved. No part of this work may be reproduced or transmitted in any form, or by any means, without the prior written permission of ERM.

www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation 20 April 2021

2nd Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

#### **CONTENTS**

1.	INTRO	RODUCTION	1
	1.1	Purpose of the Report	1
	1.2	Structure of the Report	1
2.	NOISI	SE MONITORING	2
	2.1	Introduction	2
	2.2	Noise Monitoring Requirements	2
		2.2.1 Monitoring Locations	2
		2.2.2 Monitoring Parameters	3
		2.2.3 Monitoring Frequency	
		2.2.4 Monitoring Methodology	
		2.2.5 Compliance Assessment	
2.3 2.4 3. CONC List of Appe APPENDIX A		Results of Noise Monitoring	
	2.4	Summary of Noise Exceedances	5
3.	CONC	ICLUSION	6
APP	ENDIX	A CALIBRATION CERTIFICATES OF THE NOISE MEASUREMENT	EQUIPMENT
APP	ENDIX	B RESULTS OF NOISE MONITORING	
APP	ENDIX	C PHOTOGRAPHS OF THE MONITORING STATIONS	
List	of Table		
	e 2.1	Alternative Noise Monitoring Stations	
	e 2.2	Schedule of the Shows	
	e 2.3	Noise Monitoring Schedule during this Reporting Month	
	e 2.4	Noise Measurement Equipment	
	e 2.5	Action and Limit Levels for Entertainment Noise	
Tabl	~ ? E	Compliance of Noise Monitoring during this Reporting Period	_

2nd Monthly Noise Monitoring Report (6 Mar 2021 - 5 Apr 2021)

#### 1. INTRODUCTION

ERM-Hong Kong, Limited (ERM) has been appointed by Ocean Park Corporation (OPC) to undertake noise monitoring for the first operational year of the Update of Design of the Existing Lagoon Show under the "Repositioning and Long Term Operation Plan of Ocean Park" (the Project) with an updated layout of loudspeaker clusters, as presented in the Noise Review Study Report (Noise Review 2020) deposited to the EPD on 9 January 2020.

### 1.1 Purpose of the Report

The Update of Design of the Existing Lagoon Show (including the Soul of the Ocean and Vision of Hong Kong) commenced on 19 January 2020 with the 1<sup>st</sup> noise monitoring report which presented monitoring results during the reporting period from 10 January to 9 February 2020 submitted to EPD in February 2021. The operation of Ocean Park was then temporarily closed and the lagoon show was suspended due to COVID-19 afterwards.

The operation of Ocean Park resumed on 18 February 2021 and the Vision of Hong Kong (VHK) has been relaunched since 6 March 2021. This is the 2<sup>nd</sup> noise monitoring report which summarises the impact monitoring results during the reporting period from **6 March** to **5 April 2021**.

## 1.2 Structure of the Report

After this introductory section, the remainder of this report is arranged as follows:

**Section 2** describes the noise monitoring methodology, presents the monitoring results and discusses the results; and

**Section 3** presents an overall conclusion of the noise monitoring.

www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation 20 April 2021 Page 1

2nd Monthly Noise Monitoring Report (6 Mar 2021 - 5 Apr 2021)

#### 2. NOISE MONITORING

#### 2.1 Introduction

Noise monitoring has been carried out following the requirements given in Condition 3.1 of the Environmental Permit (EP-249/2006/D) and the updated EM&A Manual. The requirements and results are detailed in the following sections.

#### 2.2 Noise Monitoring Requirements

It has been recommended in the approved EIA Report for "Repositioning and Long Term Operation Plan of Ocean Park" and stated in the EM&A Manual that fixed plant noise source monitoring should be conducted during the first operational year of the Open-air Night Show at the Aqua City. Therefore, noise monitoring is carried out during the first operational year of the Update of Design of the Existing Lagoon Show to review the compliance with the noise limits and requirements stipulated in the Noise Review 2020.

The monitoring of fixed plant noise source impact is to be conducted:

• During the lagoon night show (hereinafter referred to as "lagoon night show noise monitoring")

Lagoon night show noise monitoring was carried out at all designated monitoring stations during the performance of lagoon night shows at a logging interval of 5 minutes. The noise monitoring should be conducted twice a week, i.e. once on a normal weekday and once on a general holiday or Sunday, as per the EM&A Manual.


As confirmed with OPC, lagoon night show (VHK) has been relaunched during public holidays (including Easter seasonal events from 2 to 9 April 2021) and weekends (Saturdays and Sundays) from 6 March 2021 to 25 April 2021. The other lagoon night show (Soul of the Ocean) has not been performed during this period. Based on the change in the show frequency, the need for noise monitoring during the lagoon night show was reviewed based on the monitoring results. Agreement from the IEC and approval from EPD (EPD's letter dated 25 February 2021) have been sought to reduce the monitoring frequency to once a week.

The following sections describe the detailed methodology of the fixed plant noise monitoring.

#### 2.2.1 Monitoring Locations

Noise monitoring was conducted at five alternative noise monitoring stations, which are the similar locations as that carried out during the first year of operation for the lagoon night show (ie Symbio) from January 2011 to February 2012. The five alternative noise monitoring stations are presented in *Table 2.1*, and shown in *Figure 2.1*.

www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation 20 April 2021 Page 2

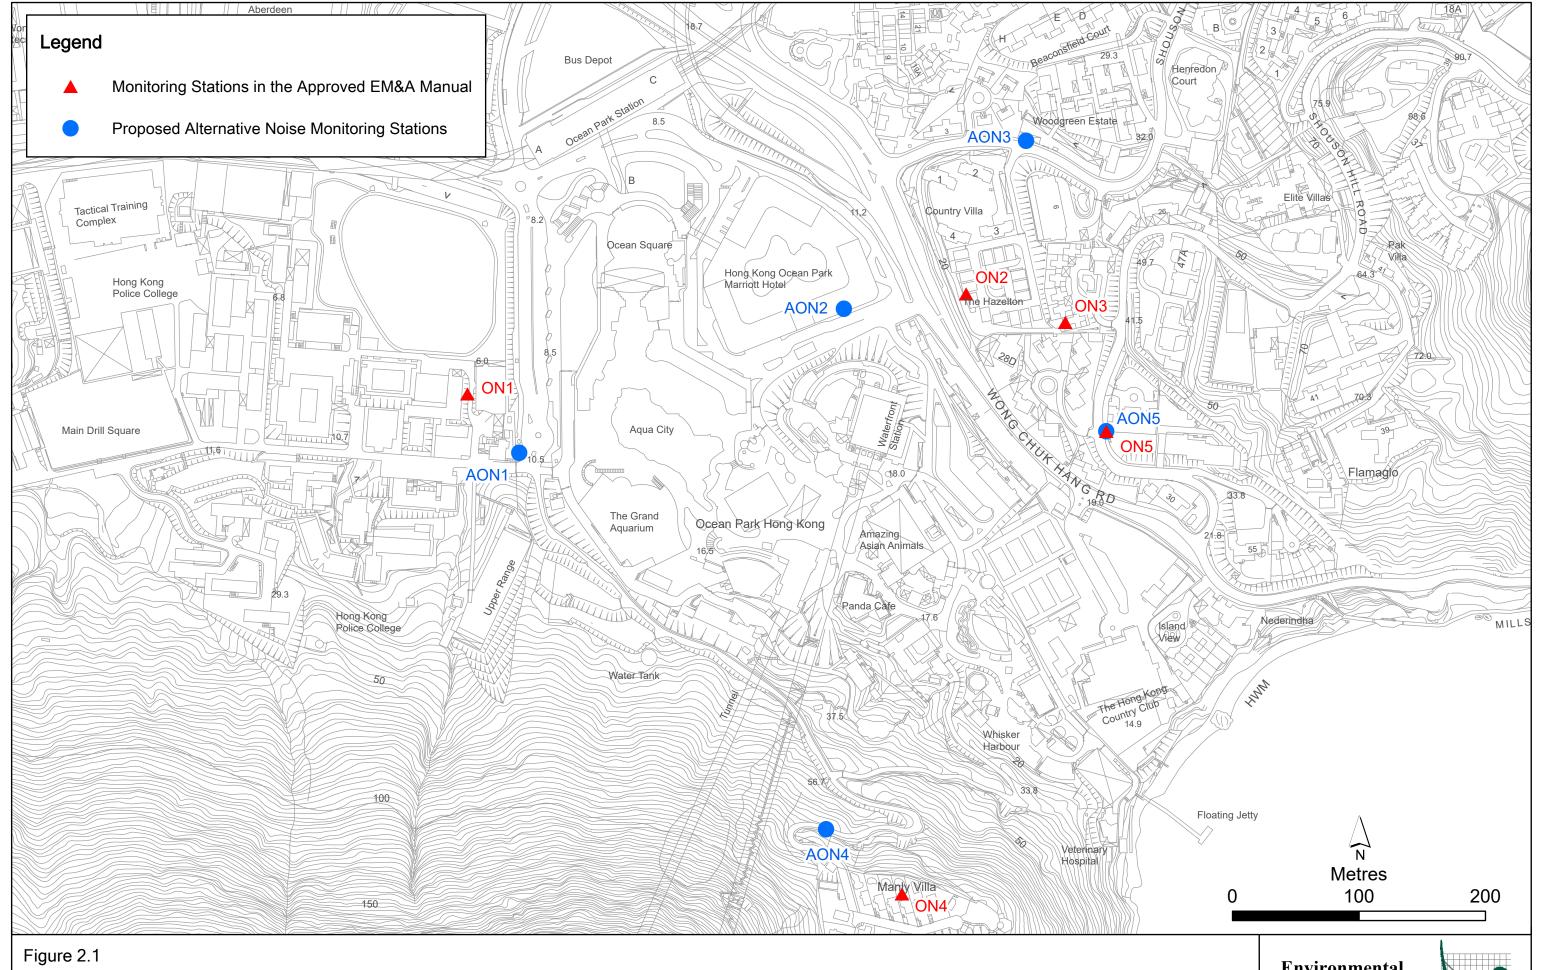

**Noise Monitoring Locations** 

Environmental Resources Management



2nd Monthly Noise Monitoring Report (6 Mar 2021 - 5 Apr 2021)

Table 2.1 Alternative Noise Monitoring Stations

Alternative Noise Monitoring Stations	Description	Location	With or without Façade Correction
AON1	Open Area adjacent to Police Training School	1.2m above street level	without façade correction
AON2	Marriott Hotel, Ocean Park	1m from façade at roof level	with façade correction
AON3	Woodgreen Estate	1.5m above street level outside boundary wall	with façade correction
AON4 <sup>(a)</sup>	Manly Villa	1.2m above street level	with façade correction
AON5	Hau Yuen	3.0m above street level outside boundary wall	with façade correction

#### Note:

(a) Due to security concern from Manly Villa, alternative noise monitoring location, AON4, has been relocated away from the entrance of Manly Villa (see Figure 2.1) which is closer to Ocean Park. Therefore, it is considered representative.

#### 2.2.2 Monitoring Parameters

### 2.2.2.1 Show Noise Monitoring

The measurements of LAeq, 5 min reading were carried out to calculate the noise level during the show with schedule shown in Table 2.2.

Table 2.2 Schedule of the Show

Description	Time
Vision of Hong Kong (VHK)	19:15-19:20 hours

## 2.2.2.2 Background Noise Level

Measurements of L<sub>Aeq. 5 min</sub> reading were carried out before and after the show when speakers were switched off to calculate the overall background noise level at each locations.

Any significant influencing factors on the measured noise levels were noted in accordance with standard acoustical principles and practices. The background-corrected noise level due to the show was computed based on the background noise level and measured noise level during the shows.

#### Monitoring Frequency 2.2.3

The noise monitoring for the show was conducted once per week. Noise monitoring schedule during this reporting month is summarised in Table 2.3.

Table 2.3 **Noise Monitoring Schedule during this Reporting Month** 

Scheduled Monitoring Date	Monitoring Stations
6 Mar 2021 (Saturday)	AON1 to AON5
13 Mar 2021 (Saturday)	AON1 to AON5
20 Mar 2021 (Saturday)	AON1 to AON5
27 Mar 2021 (Saturday)	AON1 to AON5
3 Apr 2021 (Saturday)	AON1 to AON5

#### 2.2.4 Monitoring Methodology

The sound level meters and calibrator used for the noise monitoring, as listed in Table 2.4 below, complies with IEC 651: 1979 and 804:1985 (Type 1) or equivalent international standards.

20 April 2021 www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation Page 3 2nd Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

Table 2.4 **Noise Measurement Equipment** 

Monitori	ng Location	Monitoring Equipment
AON1	Open Area adjacent to Police Training School	RION NL-52 Sound Level Meter CAL200 Calibrator
AON2	Marriott Hotel, Ocean Park	RION NL-52 Sound Level Meter CAL200 Calibrator
AON3	Woodgreen Estate	RION NL-52 Sound Level Meter CAL200 Calibrator
AON4	Manly Villa	RION NL-52 Sound Level Meter CAL200 Calibrator
AON5	Hau Yuen	RION NL-52 Sound Level Meter CAL200 Calibrator

Noise monitoring was conducted with reference to the calibration and measurement procedures as stated in the Technical Memorandum for the Assessment of Noise from Places other than Domestic Premises, Public Places or Construction Sites (IND-TM) issued under the Noise Control Ordinance (NCO). Immediately prior to and following each noise measurement the accuracy of the monitoring equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements were accepted as the calibration levels from before and after the noise measurement agree to within 1.0 dB.

The sound level meters and acoustic calibrators have been calibrated by a HOKLAS accredited laboratory every two years. The relevant calibration certificates are presented in Appendix A.

Noise measurements were conducted without the presence of fog and rain, and with steady wind speed and gusts not exceeding 5 ms<sup>-1</sup> and 10 ms<sup>-1</sup>, respectively in accordance with international standards and practices <sup>(1)</sup>. Measurement of L<sub>Aeq</sub>, L<sub>10</sub>, L<sub>90</sub>, L<sub>max</sub> and L<sub>min</sub> has been recorded for reference.

If measured noise level is affected by other noise sources at the monitoring station, eg traffic noise, such that the measured noise level is dominated by noise source other than the show, noise data will be discarded.

If measured noise level for the show is below or equal to the measured background noise level, the noise from the show is considered as insignificant and hence negligible at the monitoring location.

#### 2.2.5 Compliance Assessment

#### 2.2.5.1 Fixed Plant Noise Criteria

As recommended in the approved EIA Report and stated in the EM&A Manual, OPC will follow the Action and Limit (A/L) Levels as recommended in the approved EIA Report and EM&A Manual which are summarised in Table 2.5. In case exceedances are resulted from cumulative impacts, all steps stipulated in the Event/ Action Plan shall be followed.

**Action and Limit Levels for Entertainment Noise** Table 2.5

Identification No.	Action Level	Limit Level
ON1/AON1		L <sub>eq (5 min)</sub> 60 dB(A)
ON2/AON2	\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	$L_{eq (5 min)} 60 dB(A)$
ON3/AON3	When documented complaint is received from	L <sub>eq (5 min)</sub> 55 dB(A)
ON4/AON4	any one of the sensitive receivers	$L_{eq (5 min)} 55 dB(A)$
ON5/AON5		L <sub>eq (5 min)</sub> 55 dB(A)

<sup>(1)</sup> ISO 11819-1:1997 and ISO/FDIS 13472-1:2001

#### 2.2.5.2 Noise Criteria for Outdoor Activities

As advised by EPD, the noise levels from the outdoor activities should not be more than 5dB(A) above the prevailing background noise level during the daytime and evening periods (0700-2300 hrs), as measured at 1m from the exterior building façade of the most affected NSRs for regular outdoor activities in accordance with the *Noise Control Guidelines for Music, Singing and Instrument Performing Activities*. For the night-time period (2300-0700 hrs of the next day), the noise from outdoor events should not be audible at the nearby NSRs.

### 2.3 Results of Noise Monitoring

The results of noise monitoring conducted during this reporting period are given in *Appendix B*, with summary of compliance shown in *Table 2.6*. Photographs taken at the monitoring stations are shown in *Appendix C*.

Table 2.6 Compliance of Noise Monitoring during this Reporting Period

Date	ID		Compliance	9
		<bgl+5< th=""><th>Limit Level</th><th>Not Applicable</th></bgl+5<>	Limit Level	Not Applicable
6 Mar 2021 (Saturday)	AON1	YES	YES	-
	AON2	-	-	NA <sup>(a)</sup>
	AON3	YES	YES	-
	AON4	YES	YES	-
	AON5	-	-	NA <sup>(a)</sup>
13 Mar 2021 (Saturday)	AON1	YES	YES	-
	AON2	-	-	NA <sup>(a)</sup>
	AON3	YES	YES	-
	AON4	YES	YES	-
	AON5	YES	YES	-
20 Mar 2021 (Saturday)	AON1	YES	YES	-
	AON2	YES	YES	-
	AON3	-	-	NA <sup>(a)</sup>
	AON4	YES	YES	-
	AON5	-	-	NA <sup>(a)</sup>
27 Mar 2021 (Saturday)	AON1	YES	YES	-
	AON2	-	-	NA <sup>(a)</sup>
	AON3	YES	YES	-
	AON4	YES	YES	-
	AON5	YES	YES	-
3 Apr 2021 (Saturday)	AON1	YES	YES	-
	AON2	YES	YES	-
	AON3	-	-	NA <sup>(a)</sup>
	AON4	YES	YES	-
	AON5	-	-	NA <sup>(a)</sup>

#### Note:

## 2.4 Summary of Noise Exceedances

No record of noise exceedance during this reporting month.

www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation 20 April 2021 Page 5

<sup>(</sup>a) Noise data discarded as measurement was affected by other significant noise sources, ie truck/van, vehicle, pass-by pedestrian, passengers from cable car leaving Ocean Park, music from Hong Kong Country Club and helicopter.

2nd Monthly Noise Monitoring Report (6 Mar 2021 – 5 Apr 2021)

### 3. CONCLUSION

This is the 2<sup>nd</sup> monthly noise monitoring report which summarises the noise monitoring results during the reporting period from **6 March** to **5 April 2021**.

The noise monitoring were carried out at five designated monitoring stations during this reporting period.

No noise exceedances have been recorded during this reporting period.

www.erm.com Version: 2.0 Project No.: 0540005 Client: Ocean Park Corporation 20 April 2021 Page 6

APPENDIX A	CALIBRATION CERTIFICATES OF THE NOISE MEASUREMENT EQUIPMENT

UPDATE OF DESIGN OF THE EXISTING LAGOON SHOW IN OCEAN PARK HONG KONG



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

校正證書

Certificate No.: C203821

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-1389)

Date of Receipt / 收件日期: 30 June 2020

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion

Model No./型號

NL-52

Serial No. / 編號

00643040

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration

DATE OF TEST / 測試日期

9 July 2020

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification. (after adjustment)

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested By 測試

K P Cheuk Assistant Engineer

Certified By 核證

Lee Engineer Date of Issue 簽發日期

10 July 2020

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail 電郵: callab a suncreation.com Website/網址: www.suncreation.com



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

Certificate No.: C203821

證書編號

校正證書

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

- 2. Self-calibration using the internal standard (After Adjustment) was performed before the test 6.1.1.2 to 6.3.2.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment:

Equipment ID CL280

Description

Certificate No.

CL281

40 MHz Arbitrary Waveform Generator

C200258

Multifunction Acoustic Calibrator

CDK1806821

- 5. Test procedure: MA101N.
- 6. Results:

400

- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Adjustment

UUT Setting			Applied Value		UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	* 91.9	± 1.1

<sup>\*</sup> Out of IEC 61672 Class 1 Spec.

6.1.1.2 After Adjustment

	UUT Setting			Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

	UU'	T Setting	Applie	UUT		
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	· 1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

Website/網址: www.suncreation.com

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Page 2 of 4



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C203821

證書編號

6.2 Time Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Time Level Freq.		Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	±.0.3

### 6.3 Frequency Weighting

6.3.1 A-Weighting

Section 1	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec.
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.7	$-26.2 \pm 1.5$
					125 Hz	77.8	$-16.1 \pm 1.5$
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.7	$-3.2 \pm 1.4$
					1 kHz	94.0	Ref.
					2 kHz	95.2	$+1.2 \pm 1.6$
					4 kHz	95.0	$+1.0 \pm 1.6$
					8 kHz	93.0	-1.1 (+2.1; -3.1)
- MIT - 2					12.5 kHz	89.6	-4.3 (+3.0; -6.0)

6.3.2 C-Weighting

	UUT	Setting		Appli	ied Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	$L_{C}$	C	Fast	94.00	63 Hz	93.1	$-0.8 \pm 1.5$
					125 Hz	93.8	$-0.2 \pm 1.5$
1 1 1 1 1 1					250 Hz	94.0	$0.0 \pm 1.4$
					500 Hz	94.0	$0.0 \pm 1.4$
				1	1 kHz	94.0	Ref.
					2 kHz	93.8	$-0.2 \pm 1.6$
					4 kHz	93.2	$-0.8 \pm 1.6$
		1			8 kHz	91.1	-3.0 (+2.1; -3.1)
					12.5 kHz	87.6	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

Certificate No.: C203821

證書編號

校正證書

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 06829

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value: 94 dB : 63 Hz - 125 Hz  $: \pm 0.35 \text{ dB}$ 

250 Hz - 500 Hz  $: \pm 0.30 \text{ dB}$ 1 kHz  $: \pm 0.20 \text{ dB}$ 2 kHz - 4 kHz  $: \pm 0.35 \, dB$ 8 kHz  $: \pm 0.45 \text{ dB}$ 12.5 kHz  $: \pm 0.70 \text{ dB}$ 

104 dB: 1 kHz  $: \pm 0.10 \text{ dB (Ref. 94 dB)}$ 114 dB: 1 kHz  $: \pm 0.10 \text{ dB (Ref. 94 dB)}$ 

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C202701

證書編號

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-0981)

Date of Receipt / 收件日期: 7 May 2020

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion NL-52

Model No. / 型號 Serial No./編號

00643039

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration

18 May 2020

TEST RESULTS / 測試結果

DATE OF TEST / 測試日期

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification. (after adjustment)

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Assistant Engineer

Certified By

Lee

Date of Issue 簽發日期

22 May 2020

核證

Engineer

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

校正證書

Certificate No.: C20

C202701

證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the internal standard (After Adjustment) was performed before the test 6.1.1.2 to 6.3.2.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment:

Equipment ID

Description

Certificate No.

CL280 CL281 40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator C200258

CDK1806821

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Adjustment

	UUT Setting				d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	* 97.3	± 1.1

<sup>\*</sup> Out of IEC 61672 Class 1 Spec.

6.1.1.2 After Adjustment

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

	UU'	T Setting	Applie	d Value	UUT	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	$L_{A}$	A	Fast	94.00 104.00	• 1	94.0 (Ref.) 104.0
	16,			114.00		114.0

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: 0

C202701

證書編號

6.2 Time Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	cy Time Level Fr		Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	$\pm 0.3$

## 6.3 Frequency Weighting

6.3.1 A-Weighting

	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.7	$-26.2 \pm 1.5$
					125 Hz	77.8	$-16.1 \pm 1.5$
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.8	$-3.2 \pm 1.4$
					1 kHz	94.0	Ref.
					2 kHz	95.3	$+1.2 \pm 1.6$
					4 kHz	95.1	$+1.0 \pm 1.6$
					8 kHz	93.0	-1.1 (+2.1; -3.1)
					12.5 kHz	89.6	-4.3 (+3.0 ; -6.0

6.3.2 C-Weighting

	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	93.2	$-0.8 \pm 1.5$
			the same of		125 Hz	93.9	$-0.2 \pm 1.5$
			1 1 1 1 1 1 1		250 Hz	94.0	$0.0 \pm 1.4$
				- 7	500 Hz	94.0	$0.0 \pm 1.4$
					1 kHz	94.0	Ref.
			3 1 de 15 15 15 15 15 15 15 15 15 15 15 15 15		2 kHz	93.9	$-0.2 \pm 1.6$
					4 kHz	93.2	-0.8 ± 1.6
					8 kHz	91.1	-3.0 (+2.1; -3.1)
					12.5 kHz	87.7	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



## Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C202701

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 12128

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz :  $\pm$  0.35 dB

104 dB : 1 kHz :  $\pm$  0.10 dB (Ref. 94 dB) 114 dB : 1 kHz :  $\pm$  0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

Certificate No.:

C203481

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-1282)

Date of Receipt / 收件日期: 15 June 2020

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion

Model No./型號 Serial No./編號

NL-52 00331806

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}$ C Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$ 

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規節

Calibration check

DATE OF TEST / 測試日期

23 June 2020

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested By

測試

4

K P Cheuk Assistant Engineer

Certified By

核證

K C Lee Engineer Date of Issue 簽發日期

29 June 2020

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓 Tel/電話: (852) 2927 2606 E-mail/電郵: callab@suncreation.com

Fax/傳真: (852) 2744 8986

Website/網址: www.suncreation.com



## Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C203481

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment:

Equipment ID

Description

Certificate No.

CL280 CL281 40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator C200258

CDK1806821

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	93.7	± 1.1

6.1.2 Linearity

	UUT Setting				d Value	UUT
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	$L_A$	A	Fast	94.00	1	93.7 (Ref.)
				104.00		103.7
				114.00		113.7

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

6.2 Time Weighting

	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	93.7	Ref.
			Slow		C2-20-01	93.7	$\pm 0.3$

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



## Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C203481

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

And the second second	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.4	-26.2 ± 1.5
					125 Hz	77.5	$-16.1 \pm 1.5$
					250 Hz	85.0	$-8.6 \pm 1.4$
					500 Hz	90.5	$-3.2 \pm 1.4$
					1 kHz	93.7	Ref.
					2 kHz	94.9	$+1.2 \pm 1.6$
					4 kHz	94.7	$+1.0 \pm 1.6$
					8 kHz	92.7	-1.1 (+2.1; -3.1)
					12.5 kHz	89.3	-4.3 (+3.0; -6.0)

6.3.2 C-Weighting

	UUT	Setting		Appli	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>C</sub>	С	Fast	94.00	63 Hz	92.8	$-0.8 \pm 1.5$
					125 Hz	93.5	$-0.2 \pm 1.5$
					250 Hz	93.7	$0.0 \pm 1.4$
					500 Hz	93.7	$0.0 \pm 1.4$
			30 2E (K)		1 kHz	93.7	Ref.
					2 kHz	93.5	$-0.2 \pm 1.6$
					4 kHz	92.9	$-0.8 \pm 1.6$
					8 kHz	90.8	-3.0 (+2.1; -3.1)
					12.5 kHz	87.3	-6.2 (+3.0; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C203481

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 12128

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz :  $\pm$  0.35 dB

104 dB: 1 kHz : ± 0.10 dB (Ref. 94 dB) 114 dB: 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C206812

證書編號

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-2542) Date of Receipt / 收件日期: 26 November 2020

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商 Model No. / 型號 Rion NL-52

Serial No. / 編號

00131628

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

#### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度:

 $(50 \pm 25)\%$ 

Line Voltage / 電壓 : --

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

12 December 2020

#### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

H T Wong Assistant Engineer

Certified By 核證

K C Lee

Date of Issue 簽發日期

14 December 2020

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 - 校正及檢測實驗所
c/o 香港新界屯門與安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com



## Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C206812

證書編號

以此应目

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

CL280

Description

40 MHz Arbitrary Waveform Generator

Certificate No.

C200258

CL281

Multifunction Acoustic Calibrator

CDK1806821

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)	- A	Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.6	± 1.1

6.1.2 Linearity

	UU	T Setting		Applie	d Value	UUT
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	93.6 (Ref.)
				104.00		103.6
				114.00		113.7

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

6.2 Time Weighting

	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_A$	A	Fast .	94.00	1 .	93.6	Ref.
	15.61		Slow			93.6	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C206812

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

	UUT	Setting		Appl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_A$	A	Fast	94.00	63 Hz	67.3	$-26.2 \pm 1.5$
					125 Hz	77.4	$-16.1 \pm 1.5$
					250 Hz	84.9	-8.6 ± 1.4
					500 Hz	90.3	$-3.2 \pm 1.4$
		fill it was the		11'-5'	1 kHz	93.6	Ref.
		a715a 1511	1%		2 kHz	94.8	$+1.2 \pm 1.6$
				1.77	4 kHz	94.6	$+1.0 \pm 1.6$
					8 kHz	92.6	-1.1 (+2.1; -3.1)
					12.5 kHz	89.2	-4.3 (+3.0; -6.0)

6.3.2 C-Weighting

	UUT	Setting		Appli	ed Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	92.7	$-0.8 \pm 1.5$
					125 Hz	93.4	$-0.2 \pm 1.5$
					250 Hz	93.6	$0.0 \pm 1.4$
			1 1 1 1 1 1 1		500 Hz	93.6	$0.0 \pm 1.4$
					1 kHz	93.6	Ref.
			Nge		2 kHz	93.4	-0.2 ± 1.6
					4 kHz	92.8	$-0.8 \pm 1.6$
					8 kHz	90.7	-3.0 (+2.1; -3.1)
					12.5 kHz	87.2	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C206812

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 10446

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz :  $\pm$  0.35 dB

250 Hz - 500 Hz :  $\pm 0.30 \text{ dB}$  1 kHz :  $\pm 0.20 \text{ dB}$  2 kHz - 4 kHz :  $\pm 0.35 \text{ dB}$  8 kHz :  $\pm 0.45 \text{ dB}$ 12.5 kHz :  $\pm 0.70 \text{ dB}$ 

104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB) 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校下證書

Certificate No.:

C203474

證書編號

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-1282)

Date of Receipt / 收件日期: 15 June 2020

Description / 儀器名稱

Precision Acoustic Calibrator

Manufacturer / 製造商

LARSON DAVIS

Model No. / 型號

CAL200

Serial No. / 編號

16878

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS/測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

23 June 2020

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA
- The Bruel & Kjaer Calibration Laboratory, Denmark

Tested By

測試

K P Cheuk Assistant Engineer

Certified By

核證

K C Lee

Date of Issue 簽發日期

29 June 2020

Engineer

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior

written approval of this laboratory 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 1 of 2



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration

Certificate No.: C203474

證書編號

校正證書

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

> Equipment ID CL130 CL281 TST150A

Description Certificate No. Universal Counter C193756 Multifunction Acoustic Calibrator CDK1806821 Measuring Amplifier C201309

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.9	± 0.2	± 0.2
114 dB, 1 kHz	113.9		

Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C206427

證書編號

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-2353)

Date of Receipt / 收件日期: 3 November 2020

Description / 儀器名稱 :

Precision Acoustic Calibrator

Manufacturer / 製造商

LARSON DAVIS

Model No./型號

CAL200

Serial No. / 編號 Supplied By / 委託者 16172

: Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

#### TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓 : ---

## TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

21 November 2020

#### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By

測試

K C Lee Engineer

Certified By

核證

m Un O

Engineer

Date of Issue

24 November 2020

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新界屯門與安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail



## Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C206427

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A

Description
Universal Counter
Multifunction Acoustic Calibrator
Measuring Amplifier

Certificate No. C203952 CDK1806821 C201309

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.9	± 0.2	± 0.2
114 dB, 1 kHz	113.9		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.:

C206428

證書編號

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-2353)

Date of Receipt / 收件日期: 3 November 2020

Description / 儀器名稱

Precision Acoustic Calibrator

Manufacturer / 製造商

LARSON DAVIS

Model No./型號

CAL200

Serial No. / 編號

10227

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS/測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

21 November 2020

TEST RESULTS / 測試結果

DATE OF TEST / 測試日期

The results apply to the particular unit-under-test only.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies

- Fluke Everett Service Center, USA

Tested By 測試

K Lee Engineer

Certified By

H C Chan

Date of Issue 簽發日期

24 November 2020

核證 Engineer

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior

written approval of this laboratory 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration

校正證書

Certificate No.: C206428

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A Description
Universal Counter
Multifunction Acoustic Calibrator
Measuring Amplifier

Certificate No. C203952 CDK1806821 C201309

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz			± 0.2
114 dB, 1 kHz	113.8		

5,2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.000	1 kHz ± 1 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 - 校正及檢測實驗所
c/o 香港新界屯門興安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C206429

證書編號

\_\_\_\_

· ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC20-2353)

Date of Receipt / 收件日期: 3 November 2020

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No. / 編號 NL-52 00710259

Supplied By / 委託者

Envirotech Services Co.

Envirolecti Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$ 

Line Voltage / 電壓 : --

TEST SPECIFICATIONS / 測試規範

Calibration check

----

21 November 2020

TEST RESULTS / 測試結果

DATE OF TEST / 測試日期

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies

- Fluke Everett Service Center, USA

Tested By 測試

K C Lee Engineer

Engineer

Certified By

H C Chan

Date of Issue 答辞口钿

24 November 2020

核證

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

written approval of this laboratory. 本證書所載校正用之測試器材均可溯源至國際標準。 局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, I Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門與安里一號四樓 Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/

Website/網址: www.suncreation.com



#### Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.:

C206429

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment:

Equipment ID

Description

Certificate No.

CL280 CL281 40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator C200258

CDK1806821

5. Test procedure: MA101N.

- 6. Results:
- 6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

101500	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	93.9	± 1.1

6.1.2 Linearity

	UUT Setting			Applied	Applied Value		
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	
30 - 130	$L_{A}$	A	Fast	94.00	1	93.9 (Ref.)	
				104.00		103.9	
				114.00		113.9	

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

6.2 Time Weighting

UUT Setting			Applie	d Value	UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	$L_{A}$	A	Fast	94.00	1	. 93.9	Ref.
			Slow			93.9	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited Calibration & Testing Laboratory

# Certificate of Calibration

校正證書

Certificate No.: C206429

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

	UUT Setting				ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.6	$-26.2 \pm 1.5$
					125 Hz	77.7	$-16.1 \pm 1.5$
					250 Hz	85.2	$-8.6 \pm 1.4$
					500 Hz	90.6	$-3.2 \pm 1.4$
					1 kHz	93.9	Ref.
		*	*		2 kHz	95.1	$+1.2 \pm 1.6$
					4 kHz	94.9	$+1.0 \pm 1.6$
					8 kHz	92.8	-1.1 (+2.1; -3.1)
					12.5 kHz	89.4	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

	UUT Setting				Applied Value		IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	$L_{C}$	C	Fast	94.00	63 Hz	93.1	$-0.8 \pm 1.5$
					125 Hz	93.7	$-0.2 \pm 1.5$
					250 Hz	93.9	$0.0 \pm 1.4$
					500 Hz	93.9	$0.0 \pm 1.4$
					1 kHz	93.9	Ref.
					2 kHz	93.7	$-0.2 \pm 1.6$
		4			4 kHz	93.1	$-0.8 \pm 1.6$
					8 kHz	90.9	-3.0 (+2.1; -3.1)
					12.5 kHz	87.5	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited Calibration & Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C206429

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 10990

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz :  $\pm$  0.35 dB

250 Hz - 500 Hz :  $\pm 0.30 \text{ dB}$  1 kHz :  $\pm 0.20 \text{ dB}$  2 kHz - 4 kHz :  $\pm 0.35 \text{ dB}$  8 kHz :  $\pm 0.45 \text{ dB}$ 12.5 kHz :  $\pm 0.70 \text{ dB}$ 

104 dB : 1 kHz :  $\pm$  0.10 dB (Ref. 94 dB)

114 dB : 1 kHz  $\pm 0.10$  dB (Ref. 94 dB)

#### Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

<sup>-</sup> The uncertainties are for a confidence probability of not less than 95 %.

UPDATE OF DESIGN OF THE EXIS	TING LAGOON SHOW IN OCEAN PARK HONG KONG	
ABBENDIV B	DECLUTO OF MODE MODIFICATION	
APPENDIX B	RESULTS OF NOISE MONITORING	

Noise Wolltoning Field Record Sheet					
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring			
Date of Monitoring:	6 March 2021 (Saturday)				
Noise Monitoring Staff:	Ho Kam Chuen				
Temperature:	20 °C				
Wind Speed:	<5 m/s				
Noise Meter Model / Identif	ication:	Rion-NL52/ 00131628			
Calibrator Model / Identifica	ation:	CAL200/ 10227			
Calibration Level before Mea	94.0				
Calibration Level after Meas	94.0				

Measurement Location:						
AON1	Open Area adjacent to Police Training School					
AON2	Marriott Hotel					
AON3	Woodgreen Estate					
AON4	Manly Villa					
AON5	Hau Yuen					

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level NCO Limit Not (BGL+5) Level Applicable	Remarks			
AON1	19:00-19:05	Background	60.4	60.1	-	-	-	-	-	-	
AON1	19:05-19:10	Background	59.2								
AON1	19:10-19:15	Background	59.4								
AON1	19:15-19:20	VHK	60.6		0.5	51.2	60.0	YES	YES	-	
AON1	19:20-19:25	Background	61.5		-	-	-	-	-	-	
AON1	19:25-19:30	Background	59.4								

### Note:

Troube Montoning Field Record Sheet					
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring			
Date of Monitoring:	6 March 2021 (Saturday)				
Noise Monitoring Staff:	Yeung Ping Fai				
Temperature:	20 °C				
Wind Speed:	<5 m/s				
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00331806			
Calibrator Model / Identifica	ation:	CAL200/ 16878			
Calibration Level before Mea	94.0				
Calibration Level after Meass	94.0				

Measurement Location:							
AON1	Open Area adjacent to Police Training School						
AON2	Marriott Hotel						
AON3	Woodgreen Estate						
AON4	Manly Villa						
AON5	Hau Yuen						

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON2	19:00-19:05	Background	62.9	64.2	-	1	1	-	-	-	
AON2	19:05-19:10	Background	61.9								
AON2	19:10-19:15	Background	62.0								
AON2	19:15-19:20	VHK	67.2		3.0	64.2	60.0	-	-	N/A	Noise from truck/van at loading and unloading bay under measurement location
AON2	19:20-19:25	Background	68.0		-	-	-	-	-	-	Noise from truck/van at loading and unloading bay under measurement location
AON2	19:25-19:30	Background	62.3								

Note:

Noise Wolltoning Freid Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Monitoring						
Date of Monitoring:	6 March 2021 (Saturday)						
Noise Monitoring Staff:	Ho Hiu Wa						
Temperature:	20 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643039					
Calibrator Model / Identifica	ation:	CAL200/ 16172					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:							
AON1	Open Area adjacent to Police Training School						
AON2	Marriott Hotel						
AON3	Woodgreen Estate						
AON4	Manly Villa						
AON5	Hau Yuen						

### Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON3	19:00-19:05	Background	66.3	65.9	-	-	-	-	-	-	
AON3	19:05-19:10	Background	64.7								
AON3	19:10-19:15	Background	66.5								
AON3	19:15-19:20	VHK	64.7		-1.2	Negligible	55.0	YES	YES	-	
AON3	19:20-19:25	Background	64.9		-	-	1	-	-	-	
AON3	19:25-19:30	Background	66.6								

#### Note:

Troise Wolltoning Tiera Record Sheet								
Project Name / GMS No.:	0540005 OPC Noise Monitoring							
Date of Monitoring:	6 March 2021 (Saturday)							
Noise Monitoring Staff:	Cheng Tse Ho							
Temperature:	20 °C							
Wind Speed:	<5 m/s							
Noise Meter Model / Identifi	cation:	Rion-NL52/ 00710259						
Calibrator Model / Identifica	ition:	CAL200/ 10227						
Calibration Level before Mea	94.0							
Calibration Level after Meass	94.0							

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON4	19:00-19:05	Background	49.1	50.4	-	-	-	-	-	-	
AON4	19:05-19:10	Background	52.9								
AON4	19:10-19:15	Background	47.8								
AON4	19:15-19:20	VHK	51.7		1.3	45.8	55.0	YES	YES	-	
AON4	19:20-19:25	Background	51.7		-	-	1	-	-	-	
AON4	19:25-19:30	Background	48.0								

### Note:

Troise Wolltoning Tiera Record Sheet								
Project Name / GMS No.:	0540005 OPC Noise Monitoring							
Date of Monitoring:	6 March 2021 (Saturday)							
Noise Monitoring Staff:	Ho Kam Fat							
Temperature:	20 °C							
Wind Speed:	<5 m/s							
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00643040						
Calibrator Model / Identifica	ation:	CAL200/ 16878						
Calibration Level before Mea	94.0							
Calibration Level after Meass	94.0							

Measurem	Measurement Location:								
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON5	19:00-19:05	Background	58.9	59.2	-	-	ı	-	-	-	
AON5	19:05-19:10	Background	59.6								
AON5	19:10-19:15	Background	60.1								
AON5	19:15-19:20	VHK	61.5		2.3	57. <i>7</i>	55.0	-	-	N/A	affected by pass-by vehicle
AON5	19:20-19:25	Background	58.2		-	-	-	-	-	-	
AON5	19:25-19:30	Background	58.7								

### Note:

Troise Wolltoning Tiera Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Monitoring						
Date of Monitoring:	13 March 2021 (Saturday	)					
Noise Monitoring Staff:	Ho Kam Chuen						
Temperature:	21 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00131628					
Calibrator Model / Identifica	ation:	CAL200/ 10227					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:								
AON1 Open Area adjacent to Police Training School								
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

### Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${\mathop{ m corrected}^{ m (a)}} \ {\mathop{ m L}_{ m eq,5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON1	19:00-19:05	Background	60.4	59.5	-	-	-	-	-	-	
AON1	19:05-19:10	Background	59.6								
AON1	19:10-19:15	Background	58.2								
AON1	19:15-19:20	VHK	59.2		-0.3	Negligible	60.0	YES	YES	-	
AON1	19:20-19:25	Background	60.6		-	-	1	-	-	-	
AON1	19:25-19:30	Background	58.2								

### Note:

Troise Wolltoning Field Record Sheet							
Project Name / GMS No.:	itoring						
Date of Monitoring:	Date of Monitoring: 13 March 2021 (Saturday)						
Noise Monitoring Staff:							
Temperature:	21 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00331806					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurem	Measurement Location:									
AON1 Open Area adjacent to Police Training School										
AON2	N2 Marriott Hotel									
AON3	Woodgreen Estate									
AON4	Manly Villa									
AON5 Hau Yuen										

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show		BGL with Show BGL	with Show - BGL	corrected(")	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON2	19:00-19:05	Background	62.8	64.4	-	-	1	-	-	-	
AON2	19:05-19:10	Background	61.9								
AON2	19:10-19:15	Background	63.1								
AON2	19:15-19:20	VHK	67.3		2.9	64.1	60.0	-	-	IN / A	affected by vehicle along Wong Chuk Hang Road
AON2	19:20-19:25	Background	68.3		-	-	-	-	-	-	affected by vehicle along Wong Chuk Hang Road
AON2	19:25-19:30	Background	62.2								

#### Note: (a)

Troise Wolltoning Tiera Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Moni	itoring					
Date of Monitoring:	13 March 2021 (Saturday)	)					
Noise Monitoring Staff:							
Temperature:	21 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00643039					
Calibrator Model / Identifica	ation:	CAL200/ 16172					
Calibration Level before Mea	94.0						
Calibration Level after Meass	94.0						

Measurem	Measurement Location:									
AON1 Open Area adjacent to Police Training School										
AON2	N2 Marriott Hotel									
AON3	Woodgreen Estate									
AON4	Manly Villa									
AON5 Hau Yuen										

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time		L <sub>eq, 5min</sub>	BGL	with Show - BGL	corrected <sup>(a)</sup> L <sub>eq, 5min</sub>	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON3	19:00-19:05	Background	64.3	65.6	-	-	ı	-	-	-	
AON3	19:05-19:10	Background	64.2								
AON3	19:10-19:15	Background	65.7								
AON3	19:15-19:20	VHK	64.7		-0.9	Negligible	55.0	YES	YES	-	
AON3	19:20-19:25	Background	67.0		-	-	-	-	-	-	
AON3	19:25-19:30	Background	66.2								

### Note:

Noise Wolfitoring Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	13 March 2021 (Saturday)	)					
Noise Monitoring Staff:							
Temperature:	21 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00710259					
Calibrator Model / Identifica	CAL200/ 10227						
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:								
AON1 Open Area adjacent to Police Training School								
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$L_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON4	19:00-19:05	Background	50.6	51.6	-	-	-	-	-	-	
AON4	19:05-19:10	Background	50.1								
AON4	19:10-19:15	Background	52.3								
AON4	19:15-19:20	VHK	55.5		3.9	53.2	55.0	YES	YES	-	
AON4	19:20-19:25	Background	53.6		-	-	1	-	-	-	
AON4	19:25-19:30	Background	50.2								

#### Note:

Noise Wolfitoring Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	13 March 2021 (Saturday)	)					
Noise Monitoring Staff:							
Temperature:	21 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643040					
Calibrator Model / Identifica	CAL200/ 16878						
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurem	Measurement Location:								
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON5	19:00-19:05	Background	55. <i>7</i>	58.4	-	-	ı	-	-	-	
AON5	19:05-19:10	Background	58.6								
AON5	19:10-19:15	Background	57.0								
AON5	19:15-19:20	VHK	58.7		0.3	46.8	55.0	YES	YES	-	
AON5	19:20-19:25	Background	60.4		-	-	1	-	-	-	
AON5	19:25-19:30	Background	58.9								

#### Note:

11020 110111011119 110101 110011							
Project Name / GMS No.:	0540005 OPC Noise Moni	itoring					
Date of Monitoring:	20 March 2021 (Saturday)						
Noise Monitoring Staff:	Ho Kam Chuen						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00131628					
Calibrator Model / Identifica	ntion:	CAL200/ 10227					
Calibration Level before Mea	94.0						
Calibration Level after Measu	94.0						

Measurem	Measurement Location:								
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{(a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON1	19:00-19:05	Background	60.4	60.5	-	-	1	-	1	-	
AON1	19:05-19:10	Background	58.8								
AON1	19:10-19:15	Background	59.7								
AON1	19:15-19:20	VHK	60.1		-0.4	Negligible	60.0	YES	YES	-	
AON1	19:20-19:25	Background	60.7		-	-	-	-	-	-	
AON1	19:25-19:30	Background	62.3								

#### Note: (a)

0							
0540005 OPC Noise Moni	toring						
20 March 2021 (Saturday)							
Yeung Ping Fai							
24 °C							
<5 m/s							
ication:	Rion-NL52/ 00331806						
ntion:	CAL200/ 16878						
Calibration Level before Measurement (dB(A)):							
Calibration Level after Measurement (dB(A)):							
	20 March 2021 (Saturday) Yeung Ping Fai  24 °C  <5 m/s  cation: tion: surement (dB(A)):						

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$\operatorname{Corrected}^{(a)} \ \operatorname{L_{eq,5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON2	19:00-19:05	Background	62.9	64.3	-	-	1	-	-	-	
AON2	19:05-19:10	Background	62.9								
AON2	19:10-19:15	Background	63.4								
AON2	19:15-19:20	VHK	65.8		1.5	60.4	60.0	YES	YES	-	
AON2	19:20-19:25	Background	67.4		-	-	-	-	-	-	Noise froNoise from passengers of cable car and music from the Hong Kong Country Clubm passengers of cable car
AON2	19:25-19:30	Background	62.9								

Note:

(a)

1 to be 1/10/14/15/16/14 11/16/14 11/16/14							
Project Name / GMS No.:	0540005 OPC Noise Moni	itoring					
Date of Monitoring:	20 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Ho Hiu Wa						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643039					
Calibrator Model / Identifica	ation:	CAL200/ 16172					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:									
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{(a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON3	19:00-19:05	Background	67.1	67.1	-	-	1	-	-	-	
AON3	19:05-19:10	Background	66.5								
AON3	19:10-19:15	Background	69.5								
AON3	19:15-19:20	VHK	72.1		5.0	70.5	55.0	ı	ı	N/A	affected by pass-by vehicle
AON3	19:20-19:25	Background	66.5		-	-	1	-	-	-	
AON3	19:25-19:30	Background	64.1								

### Note:

(a)

Troise Worksoning Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Moni	toring					
Date of Monitoring:	20 March 2021 (Saturday)						
Noise Monitoring Staff:	Cheng Tse Ho						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identifi	cation:	Rion-NL52/ 00710259					
Calibrator Model / Identifica	tion:	CAL200/ 10227					
Calibration Level before Mea	94.0						
Calibration Level after Measu	94.0						

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{ m (a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON4	19:00-19:05	Background	47.3	49.9	-	-	1	-	-	-	
AON4	19:05-19:10	Background	47.0								
AON4	19:10-19:15	Background	52.3								
AON4	19:15-19:20	VHK	51.2		1.3	45.3	55.0	YES	YES	,	
AON4	19:20-19:25	Background	51.5		-	-	1	-	-		
AON4	19:25-19:30	Background	48.8								

#### Note: (a)

Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	Date of Monitoring: 20 March 2021 (Saturday)						
Noise Monitoring Staff:	ise Monitoring Staff: Ho Kam Fat						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643040					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{ m (a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON5	19:00-19:05	Background	55.3	59.2	-	-	1	-	-	-	
AON5	19:05-19:10	Background	58.4								
AON5	19:10-19:15	Background	63.1								
AON5	19:15-19:20	VHK	65.8		6.6	64.7	55.0	1	-		affected by pass-by vehicle and pedestrian
AON5	19:20-19:25	Background	58.3		-	-	1	-	-	-	
AON5	19:25-19:30	Background	56.2								

### Note:

Noise Wolltoring Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	27 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Ho Kam Chuen						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00131628					
Calibrator Model / Identifica	CAL200/ 10227						
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

### Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON1	19:00-19:05	Background	54.6	59.5	-	-	-	-	-	-	
AON1	19:05-19:10	Background	60.2								
AON1	19:10-19:15	Background	58.0								
AON1	19:15-19:20	VHK	61.3		1.8	56.6	60.0	YES	YES	-	
AON1	19:20-19:25	Background	61.3		-	-	-	-	-	-	
AON1	19:25-19:30	Background	60.5								

#### Note: (a)

Troube Montaining Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	27 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Noise Monitoring Staff: Yeung Ping Fai						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00331806					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurem	Measurement Location:								
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	corrected <sup>(a)</sup>	Level	NCO	Limit	Not	Remarks
					DGE	L <sub>eq</sub> , 5min		(BGL+5)	Level	Applicable	
AON2	19:00-19:05	Background	64.9	64.8	-	-	-	-	-	-	
AON2	19:05-19:10	Background	63.3								
AON2	19:10-19:15	Background	63.3								
AON2	19:15-19:20	VHK	66.8		2.0	62.5	60.0	-	-		Noise from passengers from cable car leaving Ocean Park
AON2	19:20-19:25	Background	67.5		-	-	-	-	-	-	Noise from passengers from cable car leaving Ocean Park
AON2	19:25-19:30	Background	63.0								

### Note: (a)

Noise Wolltoring Field Record Sheet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	27 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Ho Hiu Wa						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643039					
Calibrator Model / Identifica	CAL200/ 16172						
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurem	Measurement Location:									
AON1	Open Area adjacent to Police Training School									
AON2	Marriott Hotel									
AON3	Woodgreen Estate									
AON4	Manly Villa									
AON5	Hau Yuen									

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{({ m a})} \ { m L}_{{ m eq,5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON3	19:00-19:05	Background	65.9	67.1	-	-	-	-	-	-	
AON3	19:05-19:10	Background	67.2								
AON3	19:10-19:15	Background	67.4								
AON3	19:15-19:20	VHK	65.5		-1.6	Negligible	55.0	YES	YES	-	
AON3	19:20-19:25	Background	67.7		-	-	-	-	-	-	
AON3	19:25-19:30	Background	67.0								

#### Note: (a)

Noise Wolltoring Field Record Sileet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	27 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Cheng Tse Ho						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00710259					
Calibrator Model / Identifica	ation:	CAL200/ 10227					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:									
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

### Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ ext{corrected}^{ ext{(a)}} \  ext{L}_{ ext{eq, 5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON4	19:00-19:05	Background	50.1	49.4	-	-	ı	-	-	-	
AON4	19:05-19:10	Background	47.6								
AON4	19:10-19:15	Background	48.5								
AON4	19:15-19:20	VHK	51.4		2.0	47.1	55.0	YES	YES	-	
AON4	19:20-19:25	Background	51.7		-	-	1	-	-	-	
AON4	19:25-19:30	Background	47.4								

#### Note: (a)

Noise Wolltoring Field Record Sileet							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	27 March 2021 (Saturday)	)					
Noise Monitoring Staff:	Ho Kam Fat						
Temperature:	24 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643040					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:									
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

### Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{({ m a})} \ { m L}_{{ m eq,5min}}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON5	19:00-19:05	Background	56.7	58.2	-	-	-	-	-	-	
AON5	19:05-19:10	Background	56.2								
AON5	19:10-19:15	Background	56.8								
AON5	19:15-19:20	VHK	58.8		0.6	49.7	55.0	YES	YES	-	
AON5	19:20-19:25	Background	58.3		-	-	-	-	-	-	
AON5	19:25-19:30	Background	61.1								

#### Note: (a)

<i></i>							
0540005 OPC Noise Mon	itoring						
3 April 2021 (Saturday)							
Ho Kam Chuen							
26 °C							
<5 m/s							
ication:	Rion-NL52/ 00131628						
ation:	CAL200/ 10227						
Calibration Level before Measurement (dB(A)):							
Calibration Level after Measurement (dB(A)):							
	3 April 2021 (Saturday)  Ho Kam Chuen  26 °C  <5 m/s  ication:  ation:						

Measurement Location:									
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement		Background/		Averaged	Noise Level	BG-	Limit	C	Complian	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{(a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON1	19:00-19:05	Background	62.5	62.4	-	-	-	-	-	-	
AON1	19:05-19:10	Background	61.5								
AON1	19:10-19:15	Background	62.0								
AON1	19:15-19:20	VHK	61.5		-0.9	Negligible	60.0	YES	YES	-	
AON1	19:20-19:25	Background	65.5		-	-	-	-	-	-	
AON1	19:25-19:30	Background	56.3								

### Note:

(a)

Project Name / GMS No.:	0540005 OPC Noise Moni	itoring					
Date of Monitoring:	3 April 2021 (Saturday)						
Noise Monitoring Staff:	Yeung Ping Fai						
Temperature:	26 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00331806					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meass	94.0						

Measuremo	Measurement Location:								
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement I		Background/		Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	corrected <sup>(a)</sup> L <sub>eq, 5min</sub>	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON2	19:00-19:05	Background	63.9	64.3	-	-	1	-	-	-	
AON2	19:05-19:10	Background	63.5								
AON2	19:10-19:15	Background	65.5								
AON2	19:15-19:20	VHK	65.5		1.2	59.2	60.0	YES	YES	-	
AON2	19:20-19:25	Background	66.0		-	-	1	-	-		
AON2	19:25-19:30	Background	61.4								

### Note:

(a)

110.000 1110.11101111 110001111 011001							
Project Name / GMS No.:	0540005 OPC Noise Moni	itoring					
Date of Monitoring:	3 April 2021 (Saturday)						
Noise Monitoring Staff:	Noise Monitoring Staff: Ho Hiu Wa						
Temperature:	26 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identifi	ication:	Rion-NL52/ 00643039					
Calibrator Model / Identifica	ation:	CAL200/ 16172					
Calibration Level before Mea	94.0						
Calibration Level after Meass	94.0						

Measurement Location:									
AON1	Open Area adjacent to Police Training School								
AON2	Marriott Hotel								
AON3	Woodgreen Estate								
AON4	Manly Villa								
AON5	Hau Yuen								

# Measurement Results (dB(A)):

Measurement	Measurement			Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	Background/ With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	$ m corrected^{(a)} \ L_{eq, 5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON3	19:00-19:05	Background	64.3	66.5	-	-	1	-	-	-	
AON3	19:05-19:10	Background	68.5								affected by helicopter
AON3	19:10-19:15	Background	65.9								affected by helicopter
AON3	19:15-19:20	VHK	67.6		1.1	61.2	55.0	1	-	N/A	affected by helicopter
AON3	19:20-19:25	Background	67.3		-	-	1	-	-	-	affected by helicopter
AON3	19:25-19:30	Background	64.9								

### Note:

Troube internating treat receive ones							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	3 April 2021 (Saturday)						
Noise Monitoring Staff:							
Temperature:	26 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00710259					
Calibrator Model / Identifica	ation:	CAL200/ 10227					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						

Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement	Measurement B			Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location Time	Time	Background/ With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	corrected <sup>(a)</sup> L <sub>eq, 5min</sub>	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON4	19:00-19:05	Background	52.8	53.7	-	-	1	-	-	-	
AON4	19:05-19:10	Background	52.4								
AON4	19:10-19:15	Background	52.8								
AON4	19:15-19:20	VHK	53.8		0.1	34.5	55.0	YES	YES		
AON4	19:20-19:25	Background	57.6		-	-	1	-	-		
AON4	19:25-19:30	Background	47.4								

Note: (a)

Troube internating treat receive ones							
Project Name / GMS No.:	0540005 OPC Noise Mon	itoring					
Date of Monitoring:	3 April 2021 (Saturday)						
Noise Monitoring Staff:							
Temperature:	26 °C						
Wind Speed:	<5 m/s						
Noise Meter Model / Identif	ication:	Rion-NL52/ 00643040					
Calibrator Model / Identifica	ation:	CAL200/ 16878					
Calibration Level before Mea	94.0						
Calibration Level after Meas	94.0						


Measurement Location:								
AON1	Open Area adjacent to Police Training School							
AON2	Marriott Hotel							
AON3	Woodgreen Estate							
AON4	Manly Villa							
AON5	Hau Yuen							

# Measurement Results (dB(A)):

Measurement	Measurement B			Averaged	Noise Level	BG-	Limit	(	Complia	nce	
Location	Time	Background/ With Show	L <sub>eq, 5min</sub>	BGL	with Show - BGL	${ m corrected}^{ m (a)} \ { m L}_{ m eq,5min}$	Level	NCO (BGL+5)	Limit Level	Not Applicable	Remarks
AON5	19:00-19:05	Background	60.2	57.9	-	-	1	-	1	-	affected by helicopter
AON5	19:05-19:10	Background	55.2								affected by helicopter
AON5	19:10-19:15	Background	57.6								affected by helicopter
AON5	19:15-19:20	VHK	60.1		2.2	56.0	55.0	-	1	N/A	affected by helicopter
AON5	19:20-19:25	Background	58.9		-	-	,	-	1	-	affected by helicopter
AON5	19:25-19:30	Background	55.8								

Note: (a)


UPDATE OF DESIGN OF THE EXIS	STING LAGOON SHOW IN OCEAN PARK HONG KONG	
ADDENIDIY C	PHOTOGRAPHS OF THE MONITORING STATIONS	
AFFEINDIX C	PHOTOGRAPHS OF THE MONITORING STATIONS	

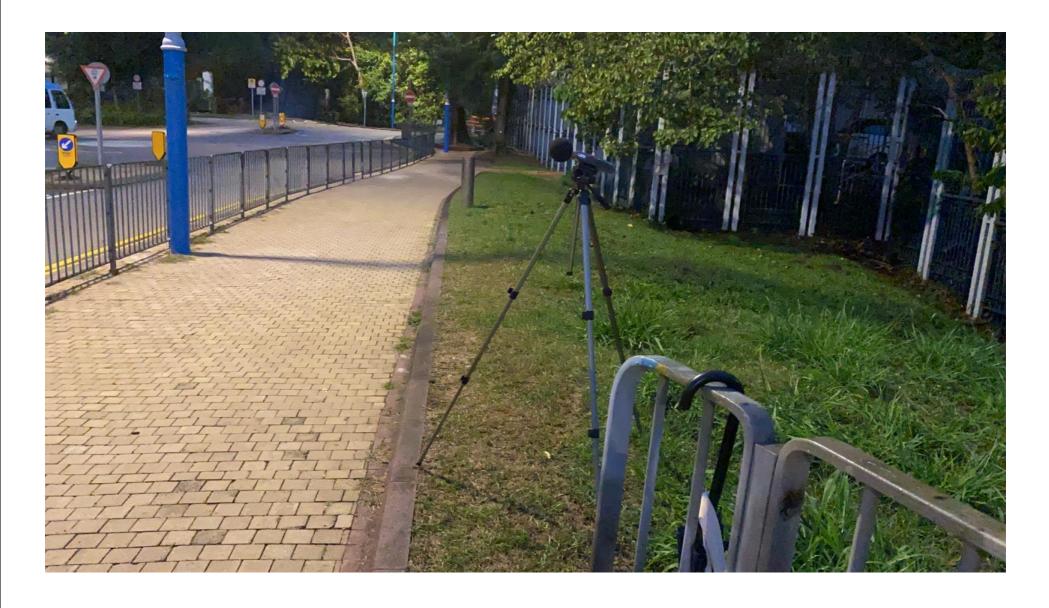

Open Area adjacent to Police Training School (AON1)

Environmental Resources Management



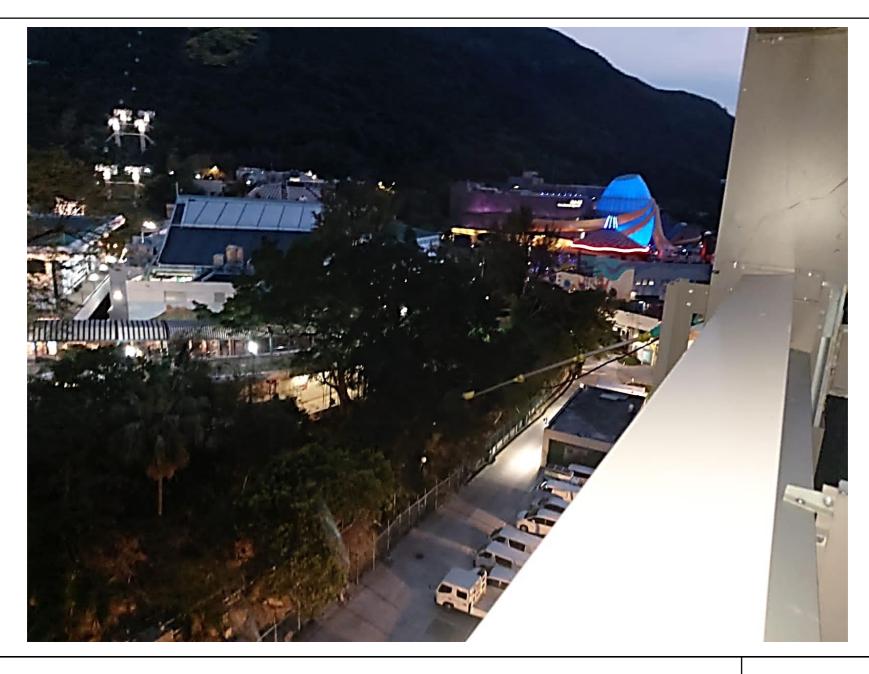

Marriot Hotel, Ocean Park (AON2)

Environmental Resources Management





Woodgreen Estate (AON3)






Manly Villa (AON4)

Environmental Resources Management



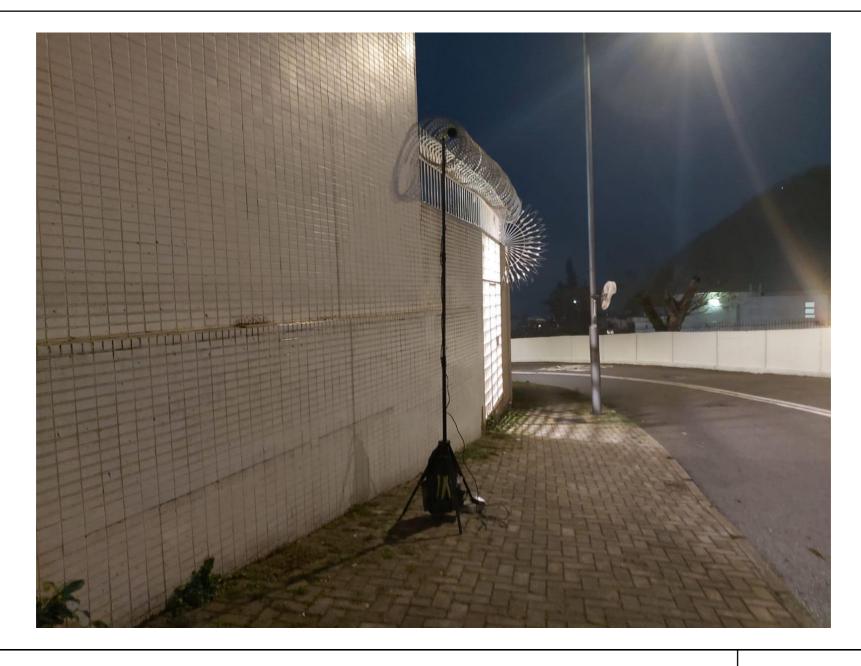

Hau Yuen (AON5)

Environmental Resources Management



# ERM has over 160 offices across the following countries and territories worldwide

Argentina New Zealand Australia Norway Belgium Panama Brazil Peru Canada Poland China Portugal Colombia Puerto Rico France Romania Germany Russia Hong Kong Singapore Hungary South Africa India South Korea Indonesia Spain Ireland Sweden Italy Switzerland Japan Taiwan Kazakhstan Thailand Kenya UAE Malaysia UK Mexico US Myanmar Vietnam

The Netherlands

#### **ERM-Hong Kong, Limited**

2509, 25/F One Harbourfront

18 Tak Fung Street

Hunghom Kowloon Hong Kong

T: +852 2271 3000 F: +852 2723 5660

www.erm.com

