

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Report No.: 0064/18/ED/0621B

MONTHLY EM&A REPORT

October 2021

Client : Civil Engineering and Development
Department, HKSAR


Contract No. : NDO 03/2018

Contract Name : Road Widening and Retrofitting Noise Barriers
on Tai Po Road (Sha Tin Section)

Report No. : 0064/18/ED/0621B

Prepared by : Tommy Ho

Reviewed by : Rex Chow

Certified by : 

David Hung
Environmental Team Leader
Fugro Technical Services Limited



Our ref: PL-202111022

Unit 2813, Level 28,
Tower I, Metroplaza,
223 Hing Fong Road, Kwai Fong,
N.T., Hong Kong.

Attention: Mr. Joseph YAN

11 November 2021

Dear Joseph,

NE/2017/05

**Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)
Monthly EM&A Report for October 2021**

I refer to the email of the ET regarding to the captioned Monthly EM&A Report with report No. 0064/18/ED/0621B, I have no adverse comment on it and verify this monthly report according to section 1.9 of the Environmental Permit with Permit No. EP- 463/2013/B.

Yours faithfully,

A handwritten signature in black ink, appearing to be 'Li Wai Ming Kevin'.

Li Wai Ming Kevin
Independent Environmental Checker

cc. CRE – Mr. YU Albert (by email only: albert.yu@aecom.com)
CEDD – Mr. YAN Joseph (by email only: jkcyan@cedd.gov.hk)



FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre

5 Lok Yi Street, Tai Lam

Tuen Mun, NT

Hong Kong

Date 12 November 2021

Our Ref. MCL/ED/0443/2021/C

The EIA Ordinance Register Office
Environmental Protection Department
27/F, Southorn Centre,
130 Hennessy Road, Wan Chai, Hong Kong
Attn: Ms. LAU Yee Ching, Eva

BY HAND & E-MAIL

Dear Ms. Lau,

Contract No. NE/2017/05

Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

Environmental Permit: EP-463/2013B

Submission of Monthly EM&A Report October 2021 (0064/18/ED/0621B)

Pursuant to EP-463/2013/B Condition 3.4, we hereby submit three hardcopies and two e-copy of the monthly EM&A Report (0064/18/ED/0621B) for your retention. This monthly EM&A Report has been certified by ETL and verified by IEC accordingly.

Thank you for your attention, should there be any comments or queries, please contact our Environmental Team Leader David Hung at 3565-4371.

Yours faithfully,
for and on behalf of
FUGRO TECHNICAL SERVICES LIMITED

David Hung
Environmental Team Leader

c.c. CEDD Attn: Mr. Joseph Yan / Mr. Kevin Yip (by E-mail)
AECOM Attn: Mr. Albert Yu / Mr. Andrew Cheng / Mr. Jacky Tse / Mr. Eric Yau (by E-mail)
IEC Attn: Mr. Kevin Li / Mr. Tandy Tse (by E-mail)
CCZJV Attn: Mr. Anthony Poon / Ms. Kimberly Wong (by E-mail)

Encl.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



TABLE OF CONTENTS

EXECUTIVE SUMMARY	I
1. INTRODUCTION	1
2. AIR QUALITY	5
3. NOISE	9
4. LANDSCAPE AND VISUAL	14
5. WASTE MANAGEMENT	15
6. SITE INSPECTION	16
7. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	17
8. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	18
9. FUTURE KEY ISSUES	20
10. CONCLUSIONS	21

FIGURES

Figure 1	Project General Layout
Figure 2a	Air Monitoring Locations
Figure 2b	Noise Monitoring Locations

LIST OF APPENDICES

Appendix A	Construction Programme
Appendix B	Project Organization Chart
Appendix C	Action and Limit Levels for Air Quality and Noise
Appendix D	Calibration Certificates of Monitoring Equipment
Appendix E	Environmental Monitoring Schedules, Examination Schedules and Arrangements on Deferral of Class Resumption for All Schools
Appendix F	Air Quality Monitoring Data
Appendix G	Noise Monitoring Data
Appendix H	Event Action Plans
Appendix I	Waste Flow Table
Appendix J	Environmental Mitigation Implementation Schedule (EMIS)
Appendix K	Weather and Meteorological Conditions during Reporting Month
Appendix L	Cumulative statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions
Appendix M	Summary of Site Audit in the Reporting Month



EXECUTIVE SUMMARY

- i. The Civil Engineering and Development Department HKSAR has appointed Fugro Technical Services Limited (FTS) to undertake the Environmental Team services for the Project and implement the EM&A works.
- ii. This Monthly EM&A report presents the environmental monitoring and audit works for the period between 1 October 2021 and 31 October 2021. As informed by the Contractor, major activities in the reporting month were summarized as below table:

Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
<ul style="list-style-type: none"> • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation and Erection Works • Road Reconstruction Works and Sheet Pile Removal 	<ul style="list-style-type: none"> • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation and Erection Works • Road Reconstruction Works and Sheet Pile Removal 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Construction / Diversion of Underground Utilities, Including ELS Works and Sheet Piling • Retaining Wall Construction Works • Construction of Cycle Track Subway, Pump Room and Stem Wall Construction Works • Lagging Wall Construction Works • Construction Work for Temporary Site Access Relocation • Pre Bore H Pile Construction Works • Profile Barrier and Stem Wall Construction Works • Foundation Works for SR2 • Construction Works for N263 Bridge Deck Widening • Construction Works for SR6 Temporary Widening • ELS Works at SHA for Widening of SR3 • Piezometer for Underground Water Pressure Measurement 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation Works • Erection of 7m Height Fencing 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Construction / Diversion of Underground Utilities, Including ELS Works and Sheet Piling • Noise Barrier Foundation Works • Mini Pile Construction Works • Stem Wall and Drainage Construction Works

Breaches of the Action and Limit Levels

- iii. 24-hour and 1-hour TSP impact monitoring were carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



- iv. Day time construction noise monitoring was carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.
- v. Regular night time noise monitoring was carried out on 7, 11, 21 and 28 October 2021 respectively and no exceedance case was recorded between 2300 and 0700 of the next day during the reporting month.

Complaint, Notification of Summons and Successful Prosecution

- vi. A complaint about the noise nuisance generated from the night-time construction activities near Man Wo House, Wo Che Estate (from 25 to 28 October 2021, during 2 to 5 a.m.) was received by the EPD Regional Office (North) on 28 October 2021. The complaint was referred from EPD to ET on 5 November 2021. ET is carrying out investigation. The details of the investigation and conclusion are expected to be included in the next monthly EM&A report.

Reporting Changes

- vii. There was no reporting change in the reporting month.

Future Key Issues

- viii. The key issues to be considered in the coming reporting month include:

Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality, waste management and landscape and visual impact.



1. INTRODUCTION

1.1 Background

1.1.1 Contract No. NE/2017/05 – Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section) (TPR-ST) (hereafter referred as “the Contract”), is the Works Contract involved the construction of road widening and retrofitting noise barriers on TPR-ST.

1.1.2 The Works of road widening on TPR-ST is classified as a designated project (DP) under the Part I of Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap. 499). The scale and scope of DP is classified as below:

- Widening and reconstruction of an approximate 1.2 km long of the existing Tai Po Road (Sha Tin Section) from dual 2-lane to dual 3-lane carriageway; and improvement of the existing Sha Tin Rural Committee Road and its junctions.

1.1.3 The Environmental Monitoring and Audit (EM&A) programme under this Contract is governed by the Environmental Permit (EP) (EP No: EP-463/2013/B) and the updated EM&A Manual (Reference No.: 0064/18/ED/0122D). The Works to be executed under this Contract and corresponding EPs include but not be limited to the following main items:

(i) Road widening works of TPR-ST:

- a. widening of TPR-ST of about 1.1 kilometres between Sha Tin Rural Committee Road (STRCR) and Fo Tan Road from dual two-lane to dual three-lane;
- b. modification to the existing diamond interchange at TPR-ST / STRCR (STRCR Interchange);
- c. provision of two pedestrian lifts, re-provision of staircase and cycle track ramp at the modified STRCR Interchange;
- d. modification of existing cycle track subway no. NS30 near Sha Tin Plaza;
- e. modification of the existing footbridge no. NF40 across TPR-ST near Wo Che Street;
- f. modification of the existing footbridge no. NF66 near Fung Wo Lane;
- g. installation of noise mitigation measures between Citylink Plaza and Mei Wo House of Wo Che Estate;
- h. associated drainage works, waterworks, street lighting works and traffic control and surveillance system (TCSS).

(ii) Retrofitting of noise barriers along TPR-ST:

- (a) western section between Citylink Plaza and Scenery Court;
- (b) eastern section between Mei Wo House of Wo Che Estate and Fo Tan Road; and
- (c) associated drainage works, waterworks and street lighting works.

(iii) Associated street furniture, road marking, traffic signs, directional signs, services and utilities, and

(iv) Associated landscaping works.

1.1.4 The location and boundary of the site is shown in **Figure 1**.



1.1.5 This Monthly EM&A report is required under EP-463/2013/B Condition 3.4. It is to report the results and findings of the EM&A programme required in the updated EM&A Manual.

1.1.6 This is the 35th monthly EM&A Report which summarized the impact monitoring results and audit findings for the construction of the road widening and retrofitting noise barriers on Tai Po Road (Sha Tin Section) (TPR-ST) (hereafter referred as “the Project”) within the period between 1 October 2021 and 31 October 2021.

1.2 Project Organization

1.2.1 The project proponent was the Civil Engineering and Development Department, HKSAR (CEDD). AECOM Asia Co. Ltd. (AECOM) was commissioned by CEDD as the Engineer for the Project. Acuity Sustainability Consulting Limited – Nature & Technologies (HK) Limited Joint Venture was commissioned as the Independent Environmental Checker (IEC). China railway – China Railway First Group – Zhen Hua Engineering Joint Venture (CCZJV) was appointed as the main contractor for the construction works under the contract NE/2017/05. Fugro Technical Services Limited (FTS) was appointed as the Environmental Team (ET) by CEDD to implement the EM&A programme for the Project.

1.2.2 The organization structure is shown in **Appendix B**. The key personnel contact names and numbers for the Project are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone
Project Proponent (CEDD)	Senior Engineer	Mr. Joseph Yan	3152 3470
Engineer’s Representative (AECOM)	Chief Resident Engineer	Mr. Albert Yu	2276 0618
IEC (Acuity Sustainability Consulting Limited – Nature & Technologies (HK) Limited Joint Venture)	Independent Environmental Checker	Mr. Kevin Li	9779 2247
Main Contractor (CCZJV)	Site Agent	Mr. Anthony Poon	9811 5135
	Environmental Officer	Ms. Kimberly Wong	5222 4603
ET (FTS)	Environmental Team Leader	Mr. David Hung	3565 4371



1.3 Construction Programme and Activities

1.3.1 The construction of the Project commenced on 29 November 2018 and is expected to complete in 2023. The construction programme is shown in **Appendix A**.

1.3.2 A summary of the major construction activities undertaken in the reporting month were shown in below table:

Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
<ul style="list-style-type: none"> • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation and Erection Works • Road Reconstruction Works and Sheet Pile Removal 	<ul style="list-style-type: none"> • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation and Erection Works • Road Reconstruction Works and Sheet Pile Removal 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Construction / Diversion of Underground Utilities, Including ELS Works and Sheet Piling • Retaining Wall Construction Works • Construction of Cycle Track Subway, Pump Room and Stem Wall Construction Works • Lagging Wall Construction Works • Construction Work for Temporary Site Access Relocation • Pre Bore H Pile Construction Works • Profile Barrier and Stem Wall Construction Works • Foundation Works for SR2 • Construction Works for N263 Bridge Deck Widening • Construction Works for SR6 Temporary Widening • ELS Works at SHA for Widening of SR3 • Piezometer for Underground Water Pressure Measurement 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Noise Barrier Foundation Works • Erection of 7m Height Fencing 	<ul style="list-style-type: none"> • Trial Pits Excavation • Tree Works (Including Preservation / Felling / Pruning / Transplantation) • Road Surface Maintenance • Construction / Diversion of Underground Utilities, Including ELS Works and Sheet Piling • Noise Barrier Foundation Works • Mini Pile Construction Works • Stem Wall and Drainage Construction Works



1.4 Status of Environmental Licenses, Notifications and Permits

1.4.1 A summary of the relevant environmental licenses, permits and/or notifications on environmental protection for this Contract is presented in **Table 1.2**.

Table 1.2 Relevant Environmental Licenses, Permits and/or Notifications

Environmental License / Permit / Notification	Reference Number	Valid From	Valid Till
Environmental Permit for whole project	EP-463/2013/B	20/12/2016	Nil
Receipt of the notification of construction dust production	Form NA	27/7/2018	Nil
Construction Waste Disposal Account	7031619	17/8/2018	Nil
Chemical Waste Producer Registration	5318-758-C4314-01	06/11/2018	Nil
Effluent Discharge License (Zone 1 – 5)	WT00032446-2018	09/11/2018	30/11/2023
Effluent Discharge License (Shui Chong Street)	WT00033829-2019	25/06/2019	30/06/2024
Construction Noise Permit for Road Closure – General Night Works (Zone 1 – 5)	GW-RN0239-21	12/05/2021	11/11/2021
Construction Noise Permit for Road Closure, Road Maintenance and Modification Works (Zone 3)	GW-RN0598-21	22/08/2021	17/11/2021
Construction Noise Permit for Road Closure, General Night Works (Zone 1 – 5)	GW-RN0600-21	22/08/2021	19/02/2022
Construction Noise Permit for Road Closure, Lane Shifting Works (Zone 1 – 2)	GW-RN0636-21	05/09/2021	30/11/2021
Construction Noise Permit for Road Closure, Sheet Pile Removal and Road Reconstruction Works (Zone 1 – 2)	GW-RN0642-21	08/09/2021	06/12/2021
Construction Noise Permit for the Operation of Water Pump (Zone 1 – 5)	GW-RN0714-21	01/10/2021	31/03/2022
Construction Noise Permit for Water Mains Connection at Pei Tau Street (Zone 3)	GW-RN0775-21	28/10/2021	30/11/2021



2. AIR QUALITY

2.1 Monitoring Requirement

In accordance with the updated EM&A Manuals, 24-hour & 1-hour Total Suspended Particulates (TSP) level at the designated air quality monitoring station are required. Impact 24-hour and 1-hour TSP monitoring should be carried out at least once every 6 days. The Action and Limit Levels of the air quality monitoring are given in **Appendix C**.

2.2 Monitoring Equipment

The 24-hour and 1-hour TSP air quality monitoring was performed using High Volume Air Samplers (HVS) and portable TSP Monitors located at each of the designated monitoring station respectively.

Table 2.1 and 2.2 summarizes the equipment used in air quality monitoring.

Table 2.1 24-hour TSP Monitoring Equipment

Item	Location	Brand	Model	Equipment	Serial Number
1	AMS 5	*Sibata	Model LD-3B	Sibata Portable TSP Monitors	597305
2	AMS 7A	*Sibata	Model LD-5R	Sibata Portable TSP Monitors	620407
3	AMS 14	*Sibata	Model LD-5R	Sibata Portable TSP Monitors	620480
4	AMS 15	*Sibata	Model LD-5R	Sibata Portable TSP Monitors	882147

*Notes: As electricity supply is not available and accessible for the High Volume Samplers (HVS) at AMS 5, 7A, 14 and 15 portable Laser Particle Photometer Monitors will be utilized for 24-hour TSP monitoring instead of High Volume samplers (HVS). The correlation between HVS and the portable Laser Particle Photometer Monitors are presented in Appendix D.

Table 2.2 1-hour TSP Monitoring Equipment

Item	Location	Brand	Model	Equipment	Serial Number
1	AMS 5	Sibata	Model LD-3B	Sibata Portable TSP Monitors	597305
2	AMS 7A	Sibata	Model LD-5R	Sibata Portable TSP Monitors	620407
3	AMS 14	Sibata	Model LD-5R	Sibata Portable TSP Monitors	620480
4	AMS 15	Sibata	Model LD-5R	Sibata Portable TSP Monitors	882147

2.3 Monitoring Methodology

2.3.1 24-hour TSP air quality monitoring by High Volume Air Samplers (HVS)

HVS Installation

The following guidelines were adopted during the installation of HVS:

- Sufficient support is provided to secure the samplers against gusty wind.
- No two samplers are placed less than 2 meters apart.
- The distance between the sampler and an obstacle, such as buildings, is at least twice the height that the obstacle protrudes above the sampler.
- A minimum of 2 meters of separation from walls, parapets and penthouses is required for rooftop samples.
- A minimum of 2 meters separation from any supporting structure, measured horizontally is required.
- No furnaces or incineration flues are nearby.



- Airflow around the samplers is unrestricted.
- The samplers are more than 20 meters from the drip line.
- Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.

Filters Preparation

Fiberglass filters (provided by the HOKLAS accredited laboratory) shall be used (Note: these filters have a collection efficiency of larger than 99% for particles of 0.3 μm diameter). A HOKLAS accredited laboratory (Fugro Technical Services Limited) is responsible for the preparation of 24-hr conditioned and pre-weighed filter papers for monitoring team.

All filters are equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature is around 25°C and not variable by more than $\pm 3^\circ\text{C}$; the relative humidity (RH) is $< 50\%$ and not variable by more than $\pm 5\%$. A convenient working RH is 40%.

Operating / Analytical Procedures

Operating / analytical procedures for the air quality monitoring are highlighted as follows:

- Prior to the commencement of the dust sampling, the flow rate of the HVS are properly set (between 0.6 m^3/min and 1.7 m^3/min) in accordance with the EM&A manual. The flow rate shall be indicated on the flow rate chart.
- The power supply shall be checked to ensure the samplers worked properly.
- On sampling, the samplers shall be operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air quality monitoring station.
- The filter holding frame is then removed by loosening the four nuts and carefully a weighted and conditioned filter is centered with the stamped number upwards, on a supporting screen.
- The filter shall be aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame is tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The shelter lid shall be closed and secured with the aluminum strip.
- The timer is then programmed. Information shall be recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- After sampling, the filter shall be removed and sent to laboratory for weighing. The elapsed time is also recorded.
- Before weighing, all filters are equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than $\pm 3^\circ\text{C}$; the relative humidity (RH) should be $< 50\%$ and not vary by more than $\pm 5\%$. A convenient working RH is 40%. Weighing results are returned to MCL for further analysis of TSP concentrations collected by each filter.

2.3.2 24-hour TSP air quality monitoring by portable Laser Particle Photometer Monitors

Operating / Analytical Procedures

The measuring procedures of the 24-hr dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Pull up the air sampling inlet cover
- Change the Mode 0 to BG once
- Push Start/Stop switch once
- Turn the knob to SENSI.ADJ and press it
- Push Start/Stop switch once
- Return the knob to the position MEASURE slowly
- Push the timer set switch to set measuring time
- Remove the cap and make a measurement

Calculation of the value of 24-hr TSP concentration is given by the average of 24 calculated 1-hr TSP concentration, where the calculated 1-hr TSP concentration is given by the product of the direct reading and the K-factor based on the correlation results between the direct reading meter and high volume sampler.

2.3.3 1-hour TSP air quality monitoring

Operating / Analytical Procedures

The measuring procedures of the 1-hr dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Pull up the air sampling inlet cover
- Change the Mode 0 to BG once
- Push Start/Stop switch once
- Turn the knob to SENSI.ADJ and press it
- Push Start/Stop switch once
- Return the knob to the position MEASURE slowly
- Push the timer set switch to set measuring time
- Remove the cap and make a measurement

2.4 Maintenance / Calibration

2.4.1 24-hour TSP air quality monitoring

The following maintenance / calibration are required for the HVS:

- The high volume motors and their accessories are properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking are made to ensure that the equipment and necessary power supply are in good working condition.
- All HVS shall be calibrated (five point calibration) using Calibration Kit upon installation and thereafter in every 3 months.
- A copy of the calibration certificates for the HVS and calibrator are provided in **Appendix D**.



2.4.2 1-hour TSP air quality monitoring

The portable TSP monitor should be calibrated at 1 year intervals.

2.5 Monitoring Locations

2.5.1 The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works. According to the Hong Kong Observatory, wind direction in October 2021 are north, north east and east. The most updated locations are summarized in **Table 2.3** and shown in **Figure 2a**.

Table 2.3 Location of Air Quality Monitoring Station

Monitoring Station	Location	Land uses
AMS 5	Tin Liu	Residential Village
AMS 7A	Sheung Wo Che	Residential Village
AMS 14	Ha Wo Che	Residential Village
AMS 15	Ha Wo Che	Residential Village

2.6 Results and Observations

2.6.1 The schedule of air quality monitoring in reporting month is provided in **Appendix E**.

2.6.2 No Action / Limit Level exceedance was recorded for 24-hr and 1-hr TSP at AMS 5, 7A, 14 and 15 in the reporting month.

2.6.3 During the reporting month, major dust sources include trial pits excavation, sheet pile removal works, mini pile construction works, road reconstruction works were observed in the site. Other factors such as road traffic along Tai Po Road may affect the monitoring results.

2.6.4 The weather conditions during the monitoring are provided in **Appendix K**.

2.6.5 The monitoring data of 24-hr and 1-hr TSP are summarized in **Table 2.4 and 2.5**. Detailed monitoring data are presented in **Appendix F**.

Table 2.4 Summary of 24-hr TSP Monitoring Results

Parameter	Monitoring Station	Average (µg/m ³)	Range (µg/ m ³)	Action Level (µg/ m ³)	Limit Level (µg/ m ³)
24-hr TSP in µg/m ³	AMS 5	48	40 – 54	156	260
	AMS 7A	46	43 – 48	171	
	AMS 14	49	45 – 53	174	
	AMS 15	47	45 – 51	172	

Table 2.5 Summary of 1-hr TSP Monitoring Results

Parameter	Monitoring Station	Average (µg/m ³)	Range (µg/ m ³)	Action Level (µg/ m ³)	Limit Level (µg/ m ³)
1-hr TSP in µg/m ³	AMS 5	59	41 – 73	340	500
	AMS 7A	57	50 – 67	344	
	AMS 14	59	48 – 70	350	
	AMS 15	58	42 – 69	350	

2.6.6 The Event and Action Plan for air quality is given in **Appendix H**.



3. NOISE

3.1 Monitoring Requirement

3.1.1 In accordance with the updated EM&A Manuals, L_{eq} (30min) monitoring is conducted for at least once a week during the construction phase between 0700 and 1900 on normal weekdays at the designated monitoring locations.

3.2 Monitoring Equipment

3.2.1 The sound level meter used in noise monitoring will comply with the International Electrotechnical Commission Publication 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum issued under the Noise Control Ordinance (NCO).

3.2.2 Sound level calibrator will be used for the on-site calibration of the meter. This calibrator complies with the IEC Publication 942 (1988) Class 1 and ANSI S1.40 - 1984. Noise measurements were only accepted to be valid if the calibration levels from before and after the measurement agree to within 1.0dB.

3.2.3 Measurements shall be recorded to the nearest 0.1dB. Sound level meters are programmed to measure A-weighted equivalent continuous sound pressure level at 30-minute intervals between 0700 and 1900 on normal weekdays at least once a week when construction activities are underway.

Table 3.1 summarizes the noise monitoring equipment model being used for this project.

Table 3.1 Noise Monitoring Equipment

Item	Brand	Model	Equipment	Serial Number
1	Casella	CEL-63X Series	Integrating Sound Level Meter	1488271
2	Casella	CEL-63X Series	Integrating Sound Level Meter	1488287
3	Casella	CEL-63X Series	Integrating Sound Level Meter	1488293
4	Casella	CEL-63X Series	Integrating Sound Level Meter	1488304
5	Casella	CEL-120 Series	Calibrator	2383707
6	Casella	CEL-120 Series	Calibrator	2383886
7	Casella	CEL-120 Series	Calibrator	4358251
8	Casella	CEL-120 Series	Calibrator	5230736

3.3 Monitoring Parameters and Frequency

Table 3.2 presents the noise monitoring parameters and frequencies.

Table 3.2 Monitoring Parameters and Frequencies of Noise Monitoring

Parameter	Frequency and Period
L_{Aeq} (30min) L_{10} and L_{90} will be recorded for reference	At each station at 0700-1900 hours on normal weekdays at a frequency of once a week



3.4 Monitoring Methodology

3.4.1 The monitoring procedures are as follows:

- The monitoring station is set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 1.2m above the ground.
- The battery condition is checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time are set as follows:
 - frequency weighting : A
 - time weighting : Fast
 - measurement time : Weekly 30 minutes between 0700-1900 on normal weekdays
- Prior to and after noise measurement, the meter shall be calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement will be considered invalid and repeat of noise measurement is required after re-calibration or repair of the equipment.
- Noise monitoring should be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.
- Noise measurement should be paused during periods of high intrusive noise if possible and observation shall be recorded when intrusive noise is not avoided.
- At the end of the monitoring period, the Leq, L10 and L90 are recorded. In addition, site conditions and noise sources are recorded on a standard record sheet.

3.5 Maintenance / Calibration

3.5.1 Maintenance and Calibration procedures are as follows:

- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory.
- Relevant calibration certificates are provided in **Appendix D**.

3.6 Monitoring Locations

3.6.1 According to the updated EM&A Manual, 25 noise monitoring locations were included during the noise monitoring. The monitoring locations are summarized in **Table 3.3** and shown in **Figure 2b**.



Table 3.3 Location of Noise Monitoring Station

Monitoring Station	Location	Land Uses	Type of Measurement
NMS1	Scenery Court	Residential	Façade
NMS2	Villa Le Parc	Residential	Façade
NMS3	Hilton Plaza	Residential	Façade
NMS4	Tin Liu	Residential Village	Façade
NMS5A	Wai Wah Centre (Site Boundary)	Residential	Façade
NMS6A	Wai Wah Centre (Site Boundary)	Residential	Façade
NMS7	Tin Liu	Residential Village	Façade
NMS8	Shatin Plaza	Residential	Façade
NMS9	Lek Yuen Estate	Residential	Façade
NMS10A	Shatin Tsung Tsin School	School	Façade
NMS11	Sheung Wo Che	Residential Village	Façade
NMS12	SKH Holy Spirit Primary School	School	Façade
NMS13	Lek Yuen Estate	Residential	Façade
NMS14	Sheung Wo Che	Residential Village	Façade
NMS15	Ha Wo Che	Residential Village	Façade
NMS16	Ha Wo Che	Residential Village	Façade
NMS17	Shatin Pui Ying College	School	Façade
NMS18	Ha Wo Che	Residential Village	Façade
NMS19	Wo Che Estate	Residential	Façade
NMS20	Wo Che Estate	Residential	Façade
NMS23	Pai Tau	Residential Village	Façade
NMS24	Shatin Plaza	Residential	Façade
NMS25A	Sheung Wo Che	Residential Village	Façade
NMS26	Wo Che Estate	Residential	Façade
NMS27	Jockey Club Ti-I College	School	Façade

3.7 Results and Observations

- 3.7.1 The schedule of noise monitoring in reporting month is provided in **Appendix E**.
- 3.7.2 The exam schedules of the schools and Arrangements on Deferral of Class Resumption for All Schools are provided in **Appendix E**.
- 3.7.3 During the monitoring month, road traffic along Tai Po Road was observed which may affect the monitoring results.
- 3.7.4 According to the onsite observation, no raining was observed and no wind speed over 5 m/s was measured during the noise monitoring. The weather conditions during the monitoring month are provided in **Appendix K**.
- 3.7.5 The day time noise monitoring data are summarized in **Table 3.4**. Detailed monitoring data are presented in **Appendix G**.

Table 3.4 Summary of Day Time Noise Impact Monitoring Results

Monitoring Station	Leq (30min) Range, dB(A)	Leq (30min) Limit Level, dB(A)
	Construction Noise Level	
NMS1	63.9 – 67.3	75
NMS2	53.3 – 54.2	75
NMS3	67.9 – 68.2	75
NMS4	64.8 – 65.5	75
NMS5A	69.3 – 70.0	75
NMS6A	71.3 – 73.3	75
NMS7	64.4 – 65.3	75
NMS8	65.4 – 69.7	75
NMS9	66.0 – 70.3	75
NMS10A	62.6 – 65.4	70 ^[2]
NMS11	60.0 – 64.6	75
NMS12	63.1 – 64.8	65 & 70 ^[2,3]
NMS13	59.0 – 66.8	75
NMS14	61.6 – 64.0	75
NMS15	59.0 – 62.5	75
NMS16	61.0 – 63.0	75
NMS17	61.8 – 64.8	65 & 70 ^[2,4]
NMS18	59.1 – 61.8	75
NMS19	63.1 – 67.9	75
NMS20	61.1 – 66.8	75
NMS23	64.7 – 66.9	75
NMS24	63.0 – 68.9	75
NMS25A	58.9 – 70.4	75
NMS26	63.5 – 72.4	75
NMS27	63.7 – 65.4	70 ^[2]

Note: 1. Leq (30min) was measured at day-time (0700-1900) on normal weekdays.
 2. 70 dB (A) for schools and 65 dB (A) for schools during examination period. The school calendar are provided in **Appendix E**.
 3. The limit level was 65 dB (A) for SKH Holy Spirit Primary School (NMS 12) during 26 – 29 October 2021.
 4. The limit level was 65 dB (A) for Shatin Pui Ying College (NMS 17) during 25 – 29 October 2021.

3.7.6 Regular night time noise monitoring were conducted on 7, 11, 21 and 28 October 2021 and the results are summarized in **Table 3.5**. Detailed monitoring data are presented in **Appendix G**.



Table 3.5 Summary of Night Time Noise Impact Monitoring Results

Monitoring Station	L_{eq} (15min) Range, dB(A)	L_{eq} (15min) Limit Level, dB(A)	L_{eq} (15min) Baseline, dB(A)
	Construction Noise Level		
NMS1	58.1 – 59.9	55	61.4
NMS2	50.7 – 53.7 ^[2]	55	49.7
NMS3	60.9 – 68.8	55	70.9
NMS4	60.4 – 61.2	55	62.6
NMS5A	51.6 – 64.7 ^{[2][4]}	55	67.9
NMS6A	63.2 – 71.3	55	71.5
NMS7	45.7 – 54.0 ^[2]	55	59.0
NMS8	61.2 – 62.8	55	64.4
NMS9	50.6 – 54.4 ^[2]	55	53.5
NMS11	49.1 – 54.3 ^[2]	55	53.2
NMS13	48.2 – 56.5 ^[2]	55	57.3
NMS14	49.1 – 54.6 ^[2]	55	54.1
NMS15	56.6 – 58.0	55	58.8
NMS16	54.8 – 59.7	55	60.1
NMS18	55.3 – 59.2	55	63.2
NMS19	50.2 – 61.6 ^[2]	55	61.7
NMS20	44.4 – 55.3 ^[2]	55	57.7
NMS23	48.4 – 59.7 ^[2]	55	59.9
NMS24	46.5 – 54.7 ^[2]	55	58.0
NMS25A	43.4 – 56.0 ^[2]	55	59.7
NMS26	52.1 – 60.6 ^[2]	55	61.2

Note: 1. L_{eq} (15min) was measured at night-time (2300-0700).
2. If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, } L_{eq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

3. Detailed analysis of each monitoring location is provided in **Appendix G**.
4. Exceedance due to traffic vehicle noise was observed on 28 October 2021.

3.7.7 Day time construction noise monitoring was carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period. For night time noise monitoring, no exceedance case was recorded between 2300 and 0700 of the next day due to construction during the reporting month.

3.7.8 The Action and Limit Levels for noise impact monitoring have been set and are presented in **Appendix C**.

3.7.9 The Event and Action Plan for noise is given in **Appendix H**.



4. LANDSCAPE AND VISUAL

4.1 Audit Requirements

4.1.1 In accordance with the EM&A Manual, the landscape and visual mitigation measures during the construction phase are primarily due to those associated temporary works for the construction of retrofitting noise barriers/enclosures. To ensure compliance with the intended aims of the measures, weekly site inspections are undertaken throughout the construction period.

4.1.2 According to the updated EM&A Manual, measures to mitigate landscape and visual impacts during construction should be checked to ensure compliance with the intended aims of the measures. The progress of the engineering works shall be regularly reviewed onsite to identify the earliest practical opportunities for the landscape works to be undertaken. The ET shall report on the Contractor's compliance on a weekly basis.

4.2 Results and Observations

4.2.1 Site audits were carried out to monitor and audit the implementation of landscape and visual mitigation measures. The summary of the site audits are given in **Appendix M**.

4.2.2 No non-compliance of the landscape and visual impact was recorded in the reporting month.



5. WASTE MANAGEMENT

5.1 Audit Requirements

5.1.1 The effective management of waste arising during the construction phase will be monitored through the site audit programme. Regular audits and site inspections should be carried out to ensure that the recommended good site practices and other mitigation measures are implemented by the Contractor.

5.1.2 The audit should look at all aspects of on-site waste management practices including the waste generation, storage, recycling, transport and disposal. The aims of waste audit are:

- to ensure the waste arising from the works are handled, stored, collected, transferred and disposed of in an environmentally acceptable manner;
- verify the implementation status and evaluate the effectiveness of the mitigation measures; and
- to encourage the reuse and recycling of material.

5.2 Results and Observations

5.2.1 C&D materials and wastes sorting were carried out on site. Receptacles were available for C&D wastes and general refuse collection.

5.2.2 The amount of wastes generated by the site activities in the reporting month is shown in **Appendix I**.



6. SITE INSPECTION

6.1 Site Inspection

- 6.1.1 Site inspections were carried out weekly to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. A summary of the mitigation measures implementation schedule is provided in **Appendix J**.
- 6.1.2 In the reporting month, 4 site inspections were carried out on 7, 15, 18 and 26 October 2021. The site inspection held on 18 October 2021 was joint inspection with the IEC, ER, the Contractor and the ET during the reporting period.
- 6.1.3 The follow-up actions requested by ET and IEC during the site inspections were completed, reported by the Contractor. All the rectifications during the reporting period were fulfilled with the requirement of Proposal of Site Inspection, Deficiency and Remedial Action. No outstanding issues were reported during the reporting month. Details of observations recorded during the site inspections are summarized in **Appendix M**.



7. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

7.1 Environmental Exceedance

- 7.1.1 24-hour and 1-hour TSP impact monitoring were carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.
- 7.1.2 Day time construction noise monitoring was carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period. Regular night time noise monitoring was carried out on 7, 11, 21 and 28 October 2021 respectively and no exceedance case was recorded between 2300 and 0700 of the next day during the reporting month.

7.2 Complaints, Notification of Summons and Prosecution

- 7.2.1 According to the previous notice received from DSD (Ref: MS 8/0/CE2815/0 pt.6) on 1 September 2021 about the improperly treated water being discharged to the nearby public stormwater drainage system, a follow-up site inspection was conducted by the Environmental Protection Inspectors (EPIs) at Zone 5 south boundary on 26 October 2021. The EPIs reviewed the site condition, treatment efficiency of the temporary wastewater treatment facilities, mitigation measures to prevent muddy water generated from soil surface, discharge points and gullies condition. EPIs commented on the mitigation measure around the discharge point near WetSep TW-WS1. The bunding next to the manhole should be rectified to prevent the inflow of muddy water. EPIs reminded that mitigation measures (such as sandbags and bunding) should be provided for enclosing the area near the piling machine. It is for directing the muddy water into the temporary wastewater treatment system. EPIs also reminded regular maintenance of the temporary wastewater treatment system is needed to ensure the effluent's water quality fulfill the standard of the Water Discharge License.
- 7.2.2 A complaint about the noise nuisance generated from the night-time construction activities near Man Wo House, Wo Che Estate (from 25 to 28 October 2021, during 2 to 5 a.m.) was received by the EPD Regional Office (North) on 28 October 2021. The complaint was referred from EPD to ET on 5 November 2021. ET is carrying out investigation. The details of the investigation and conclusion are expected to be included in the next monthly EM&A report.
- 7.2.3 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix L**.

8. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

8.1 Implementation Status

8.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Review Report, the EP and the updated EM&A Manuals. The implementation status of the mitigation measures during the reporting month is summarized in **Appendix J**.

8.1.2 According to the environmental audit performed in the reporting month, the following recommendations were made:

Air Quality Impact

- Stockpile of excavated soil should be covered with tarpaulin to prevent dust impact. Also prevent the washing of excavated soil by rainwater (Zone 3, S06).
- Decolorized NRMM should be replaced with a new one (Zone 4, S6E1).

Construction Noise Impact

- No specific observation was identified in the reporting month.

Water Quality Impact

- Sandbags and tarpaulin should be provided to prevent muddy water formation, and silt outflow into the highway (Zone 3, S06).
- Stockpile of excavated soil should be covered with tarpaulin to prevent dust impact. Also prevent the washing of excavated soil by rainwater (Zone 3, S06).
- Water leakage from the barrier was observed. Water accidentally outflow to the highway should be prevented. Mitigation measures such as water collection channel and improve the site practice should be considered (Zone 3, RW6).
- Sandbags and tarpaulin should be provided to prevent muddy water formation, and silt outflow into the highway (Zone 3, S06).
- Blockage and broken surface water collection channel were observed during rainfall. The surface water collection channel should be repaired and maintained its function (Zone 5, south boundary).
- Enhance the mitigation measure of bunding around the discharge point near the Wetsep TW-WS1 to prevent the inflow of muddy water (Zone 5, south boundary).
- Mitigation measure for enclosing the area near the piling machine to prevent passage of effluent should be improved with enough sandbags / bunds (Zone 5, south boundary).

Chemical and Waste Management

- Drip tray filled with rainwater should be cleaned. The chemical container and drip tray should be covered to prevent rainfall entering (Zone 3, RW6). Coverage with tarpaulin and provide drip tray for holding the chemical containers are needed (Zone 4, S6E1).
- General refuse and wastewater generated on-site should be cleaned to minimize odour, pest and litter impacts (Zone 3, RW7).
- Chemical container should be provided with drip tray and covered properly (Zone 4, S6E1).
- Valve should be added to the drip tray to prevent chemical leakage and soil contamination (Zone 4, S6E1).

Land Contamination

- No specific observation was identified in the reporting month.

Landscape and Visual Impact

- No specific observation was identified in the reporting month.

General Condition

- No specific observation was identified in the reporting month.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Permit / Licenses

- Environmental Permit should be displayed conspicuously at the site entrance/exit for public information (Zone 3, SR6).

9. FUTURE KEY ISSUES

9.1 Construction Programme for the Next Month

During the coming reporting month, the principal work activities within the site include:

- (1) Tree Preservation, Felling, Pruning, Transplantation in Zone 1, 2 and 3.
- (2) Road Surface Maintenance in Zone 1, 2, 3, 4 and 5.
- (3) Noise Barrier Foundation Works in Zone 1, 2, 4 and 5.
- (4) Noise Barrier Erection Works in Zone 1 and 2.
- (5) Road Reconstruction Works, Sheet Pile Removal and Lane Shifting Works in Zone 1 and 2.
- (6) Trial Pits Excavation in Zone 3.
- (7) Construction, Diversion of Underground Utilities, including ELS works and Sheet Piling in Zone 3.
- (8) Retaining Wall Construction Works in Zone 3.
- (9) Construction of Cycle Track Subway, Pump Room and Stem Wall Construction Works in Zone 3.
- (10) Demolition of Existing Parapet and Lagging Wall Construction Works in Zone 3.
- (11) Pre Bore H Pile Construction Works and Steel Works Installation for Lift in Zone 3.
- (12) Profile Barrier, Stem Wall Construction Works and Foundation Works for SR2 in Zone 3.
- (13) Construction Works for N263 & N264 Bridge Deck Widening and SR6 Temporary Widening in Zone 3.
- (14) ELS Works at SHA for Widening of SR3 in Zone 3.
- (15) Piezometer for Underground Water Pressure Measurement in Zone 3.
- (16) NF40 Footbridge Construction Works in Zone 4.
- (17) Erection of 7m Height Fencing and Protection Measure for MTRC Railway in Zone 4.
- (18) Mini Pile Construction Works in Zone 5.
- (19) Stem Wall and Drainage Construction Works in Zone 5.

9.2 Key Issues for the Coming Month

- 9.2.1 Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality, waste management and landscape and visual impact.

9.3 Monitoring Schedules for the Next Month

- 9.3.1 The tentative schedules for environmental monitoring in the coming month are provided in **Appendix E**.



10. CONCLUSIONS

- 10.1.1 24-hour and 1-hour TSP impact monitoring were carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.
- 10.1.2 Day time construction noise monitoring was carried out in the reporting month, no Action / Limit Level exceedance was recorded during the period.
- 10.1.3 Regular night time noise monitoring was carried out on 7, 11, 21 and 28 October 2021, respectively and no exceedance case was recorded between 2300 and 0700 of the next day during the reporting month.
- 10.1.4 4 site inspections were carried out on 7, 15, 18 and 26 October 2021. Recommendations on mitigation measures on air quality, water quality, chemical and waste management, permits or licenses were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 10.1.5 A complaint about the noise nuisance generated from the night-time construction activities near Man Wo House, Wo Che Estate (from 25 to 28 October 2021, during 2 to 5 a.m.) was received by the EPD Regional Office (North) on 28 October 2021. The complaint was referred from EPD to ET on 5 November 2021. ET is carrying out investigation. The details of the investigation and conclusion are expected to be included in the next monthly EM&A report.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.


Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 1

Project General Layout

Project Management In-charge: Designer: FMSD Checked: BCC Approved: CWN
 49/12/18
 Pld File by: MEB
 D:\11_2018\PROJECT\TAIPO\AECOM\JOB\AECOM_DWG\AECOM\DRAWING\CONTRACT\11000C1_1001.dwg
 B0 A1 84mm x 64mm

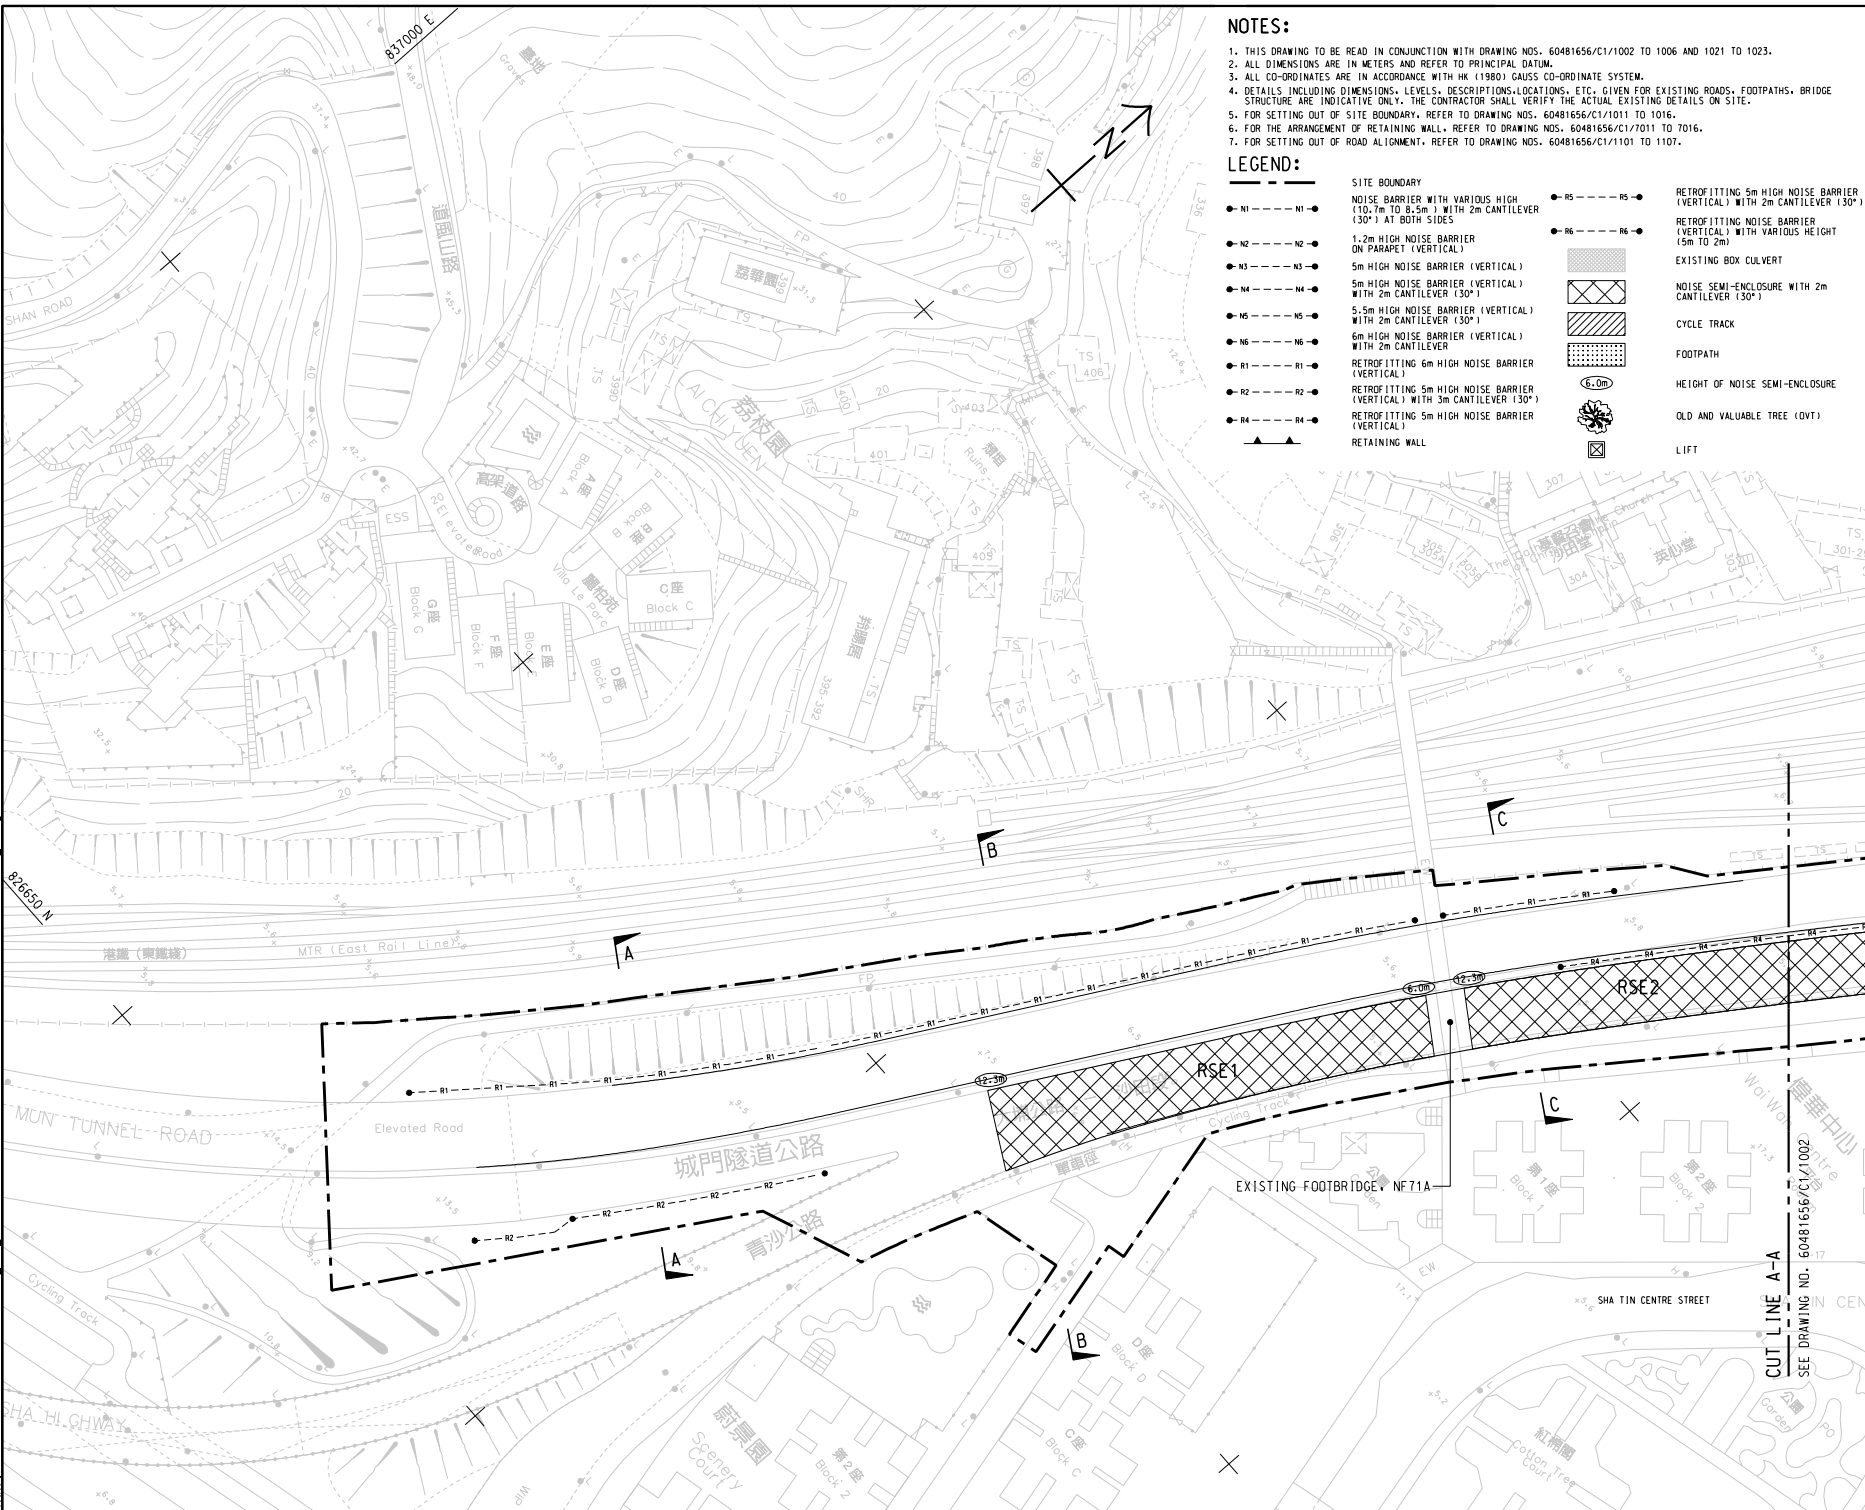

NOTES:

1. THIS DRAWING TO BE READ IN CONJUNCTION WITH DRAWING NOS. 60481656/C1/1002 TO 1006 AND 1021 TO 1023.
2. ALL DIMENSIONS ARE IN METERS AND REFER TO PRINCIPAL DATUM.
3. ALL CO-ORDINATES ARE IN ACCORDANCE WITH HK (1980) GAUSS CO-ORDINATE SYSTEM.
4. DETAILS INCLUDING DIMENSIONS, LEVELS, DESCRIPTIONS, LOCATIONS, ETC. GIVEN FOR EXISTING ROADS, FOOTPATHS, BRIDGE STRUCTURE ARE INDICATIVE ONLY. THE CONTRACTOR SHALL VERIFY THE ACTUAL EXISTING DETAILS ON SITE.
5. FOR SETTING OUT OF SITE BOUNDARY, REFER TO DRAWING NOS. 60481656/C1/1011 TO 1016.
6. FOR THE ARRANGEMENT OF RETAINING WALL, REFER TO DRAWING NOS. 60481656/C1/1011 TO 1016.
7. FOR SETTING OUT OF ROAD ALIGNMENT, REFER TO DRAWING NOS. 60481656/C1/1101 TO 1107.

LEGEND:

- | | | | |
|---------------|--|------------------------|--|
| ● N1 --- N1 ● | NOISE BARRIER WITH VARIOUS HIGH (10.7m TO 8.5m) WITH 2m CANTILEVER (30°) AT BOTH SIDES | ● R5 --- R5 ● | RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°) |
| ● N2 --- N2 ● | 1.2m HIGH NOISE BARRIER ON PARAMET (VERTICAL) | ● R6 --- R6 ● | RETROFITTING NOISE BARRIER (VERTICAL) WITH VARIOUS HEIGHT (5m TO 2m) |
| ● N3 --- N3 ● | 5m HIGH NOISE BARRIER (VERTICAL) | [Hatched Box] | EXISTING BOX CULVERT |
| ● N4 --- N4 ● | 5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°) | [Cross-hatched Box] | NOISE SEMI-ENCLOSURE WITH 2m CANTILEVER (30°) |
| ● N5 --- N5 ● | 5.5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°) | [Diagonal Hatched Box] | CYCLE TRACK |
| ● N6 --- N6 ● | 6m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER | [Dotted Box] | FOOTPATH |
| ● R1 --- R1 ● | RETROFITTING 6m HIGH NOISE BARRIER (VERTICAL) | (6.0m) | HEIGHT OF NOISE SEMI-ENCLOSURE |
| ● R2 --- R2 ● | RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL) WITH 3m CANTILEVER (30°) | [Tree Symbol] | OLD AND VALUABLE TREE (OVT) |
| ● R4 --- R4 ● | RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL) | [Wall Symbol] | RETAINING WALL |
| | | [Square with X] | LIFT |

AECOM

PROJECT
 ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
 CEDD 土木工程拓展署
 Civil Engineering and Development Department

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com


SUB-CONSULTANTS
 3AL/2016/14

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK
-	JAN 18	TENDER DRAWING	BCC

SCALE
 1:1,000 METRES

KEY PLAN
 A1:1,000




CONTRACT NO.
 NE/2017/05

SHEET TITLE
 GENERAL LAYOUT PLAN
 FIGURE 1.1 b

SHEET NUMBER
 60481656/C1/1001

SHEET 1 OF 6

15/01/2018 11:15:13
P:\1\12\18\AS\W\MT\02\H\02\KST\1\AP\06\ascom\02\02\AS\Documents\60481656\60481656\WTP-STC\AD PRODUCTION\DRAWING\CONTRACT\CI11000\CI11002.dwg
Project Management: H.H.H. (H.H.H.)
Designer: F.H.S.C. (F.H.S.C.)
Approved: C.W.N. (C.W.N.)
ISO A1 842mm x 581mm

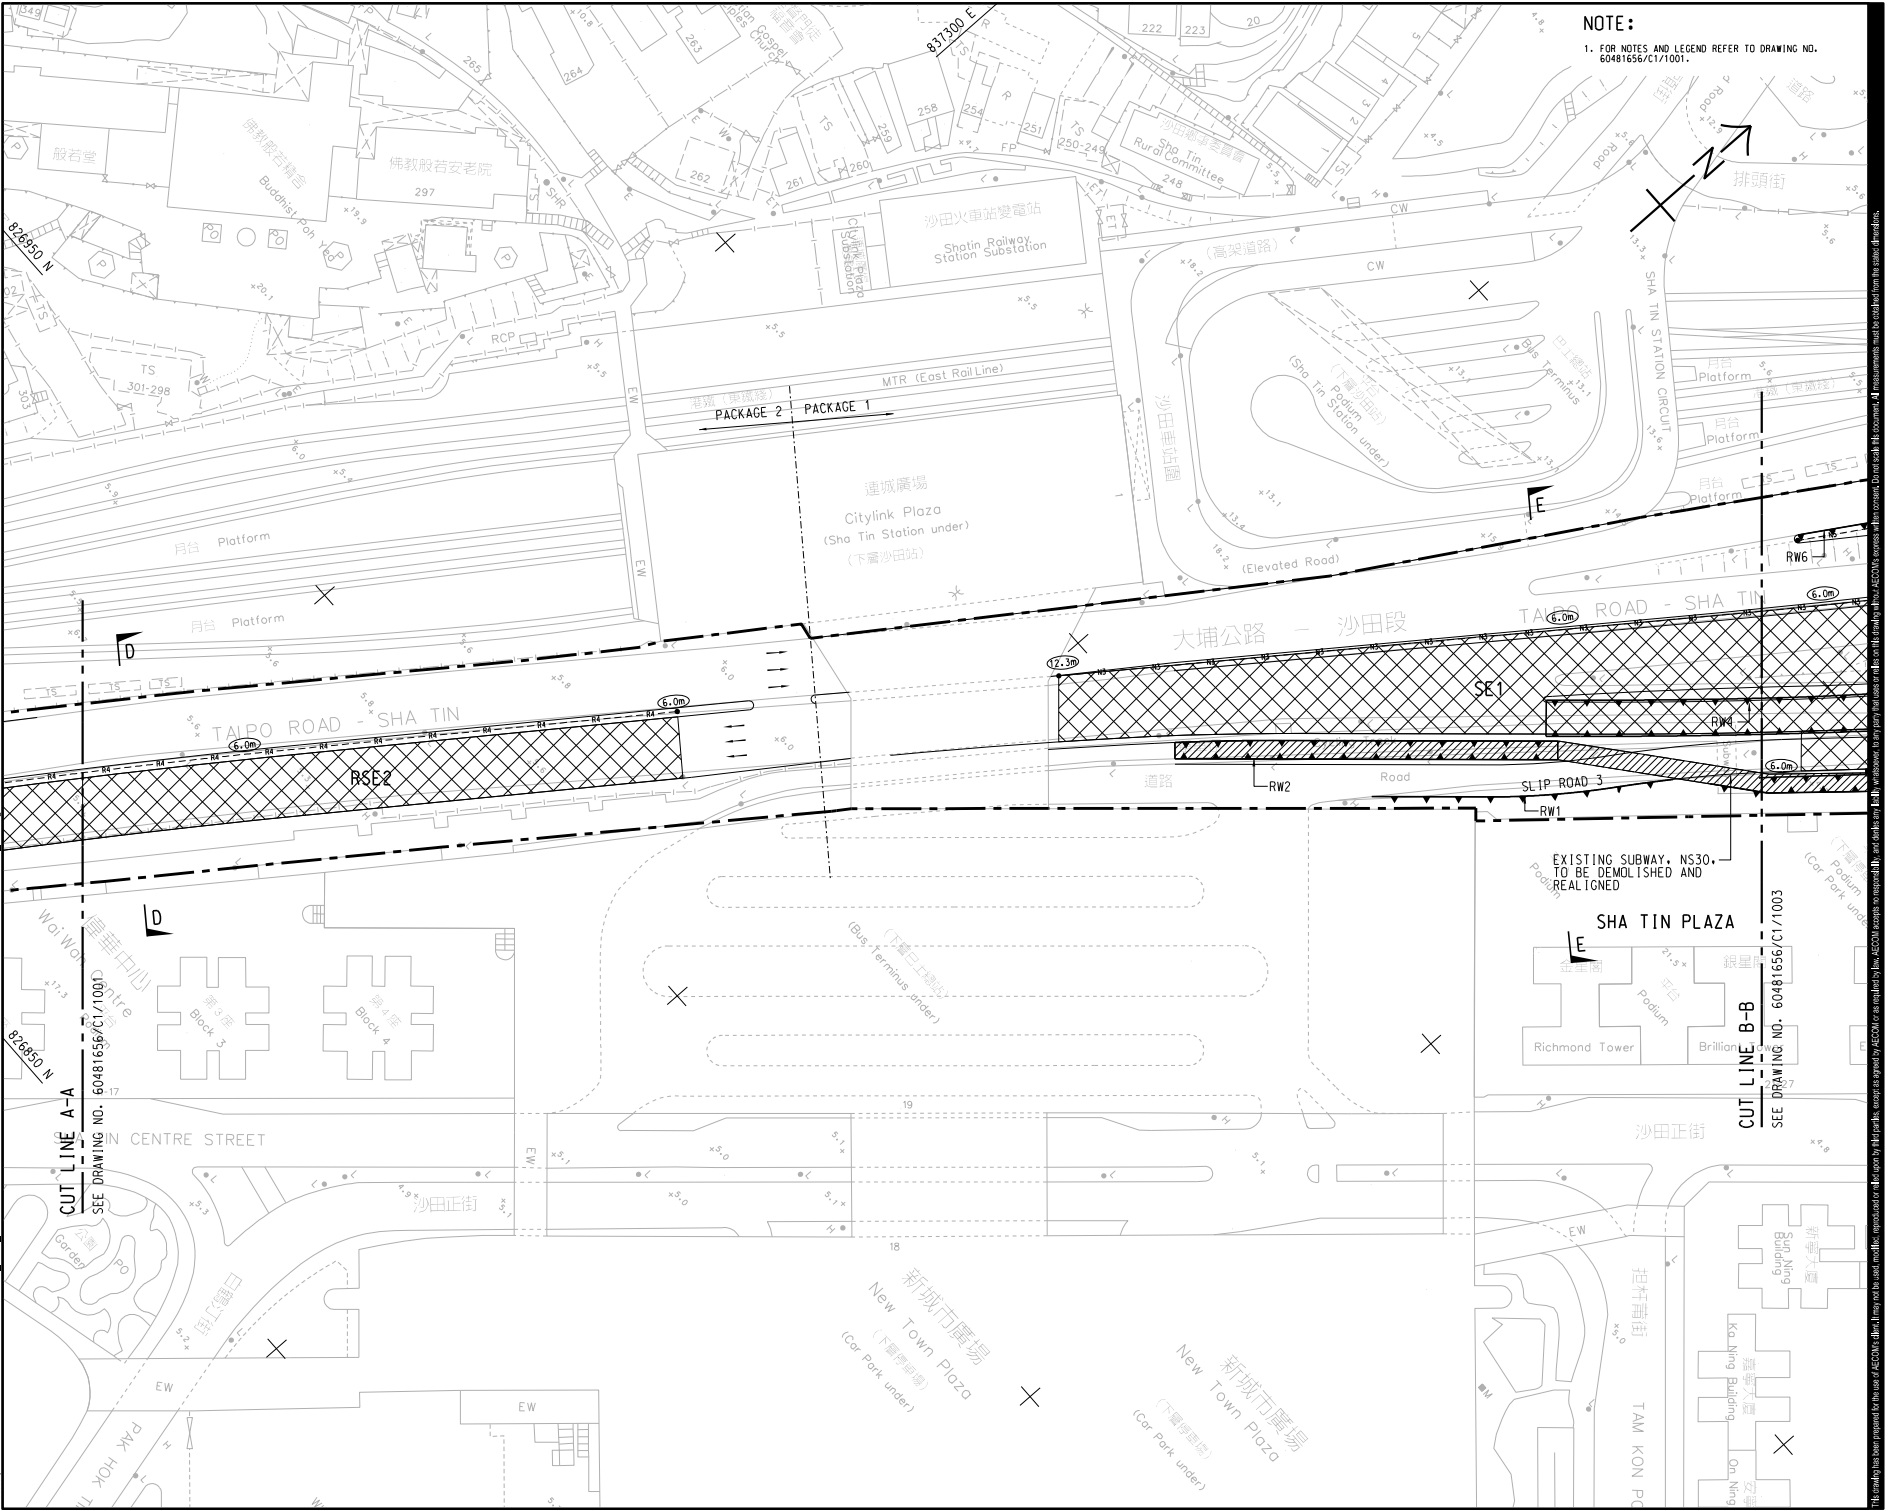

NOTE:
1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/CI11001.

AECOM

PROJECT
ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
Civil Engineering and Development Department

CONSULTANT
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
沙利工程顧問公司

ISSUE/REVISION

IR	DATE	DESCRIPTION	CHK.
-	JAN. 18	TENDER DRAWING	BCC
01		修訂	陳佩儀

STATUS
SCALE
A1 1:500
DIMENSION UNIT
METRES
KEY PLAN
A1 1:40000


CONTRACT NO.
NE/2017/05

SHEET TITLE
GENERAL LAYOUT PLAN
FIGURE 1.1b

SHEET NUMBER
60481656/CI11002

SHEET 2 OF 6

Project Management: HlBb&P
 Designer: FMSC
 Checker: BGC
 Project Management: HlBb&P
 Designer: FMSC
 Checker: BGC
 ISO A1 84mm x 61mm
 Approved CDM
 P14 File No: VLMT
 Path: \projects\civil\AECOM_D832_AS\Documents\60481656\WTP_SITCAD_PRODUCT\DRAWING\CONTRACT\1000\C1_1002.dwg
 2018/02/27
 CUT LINE B-B
 SEE DRAWING NO: 60481656/C1/1002

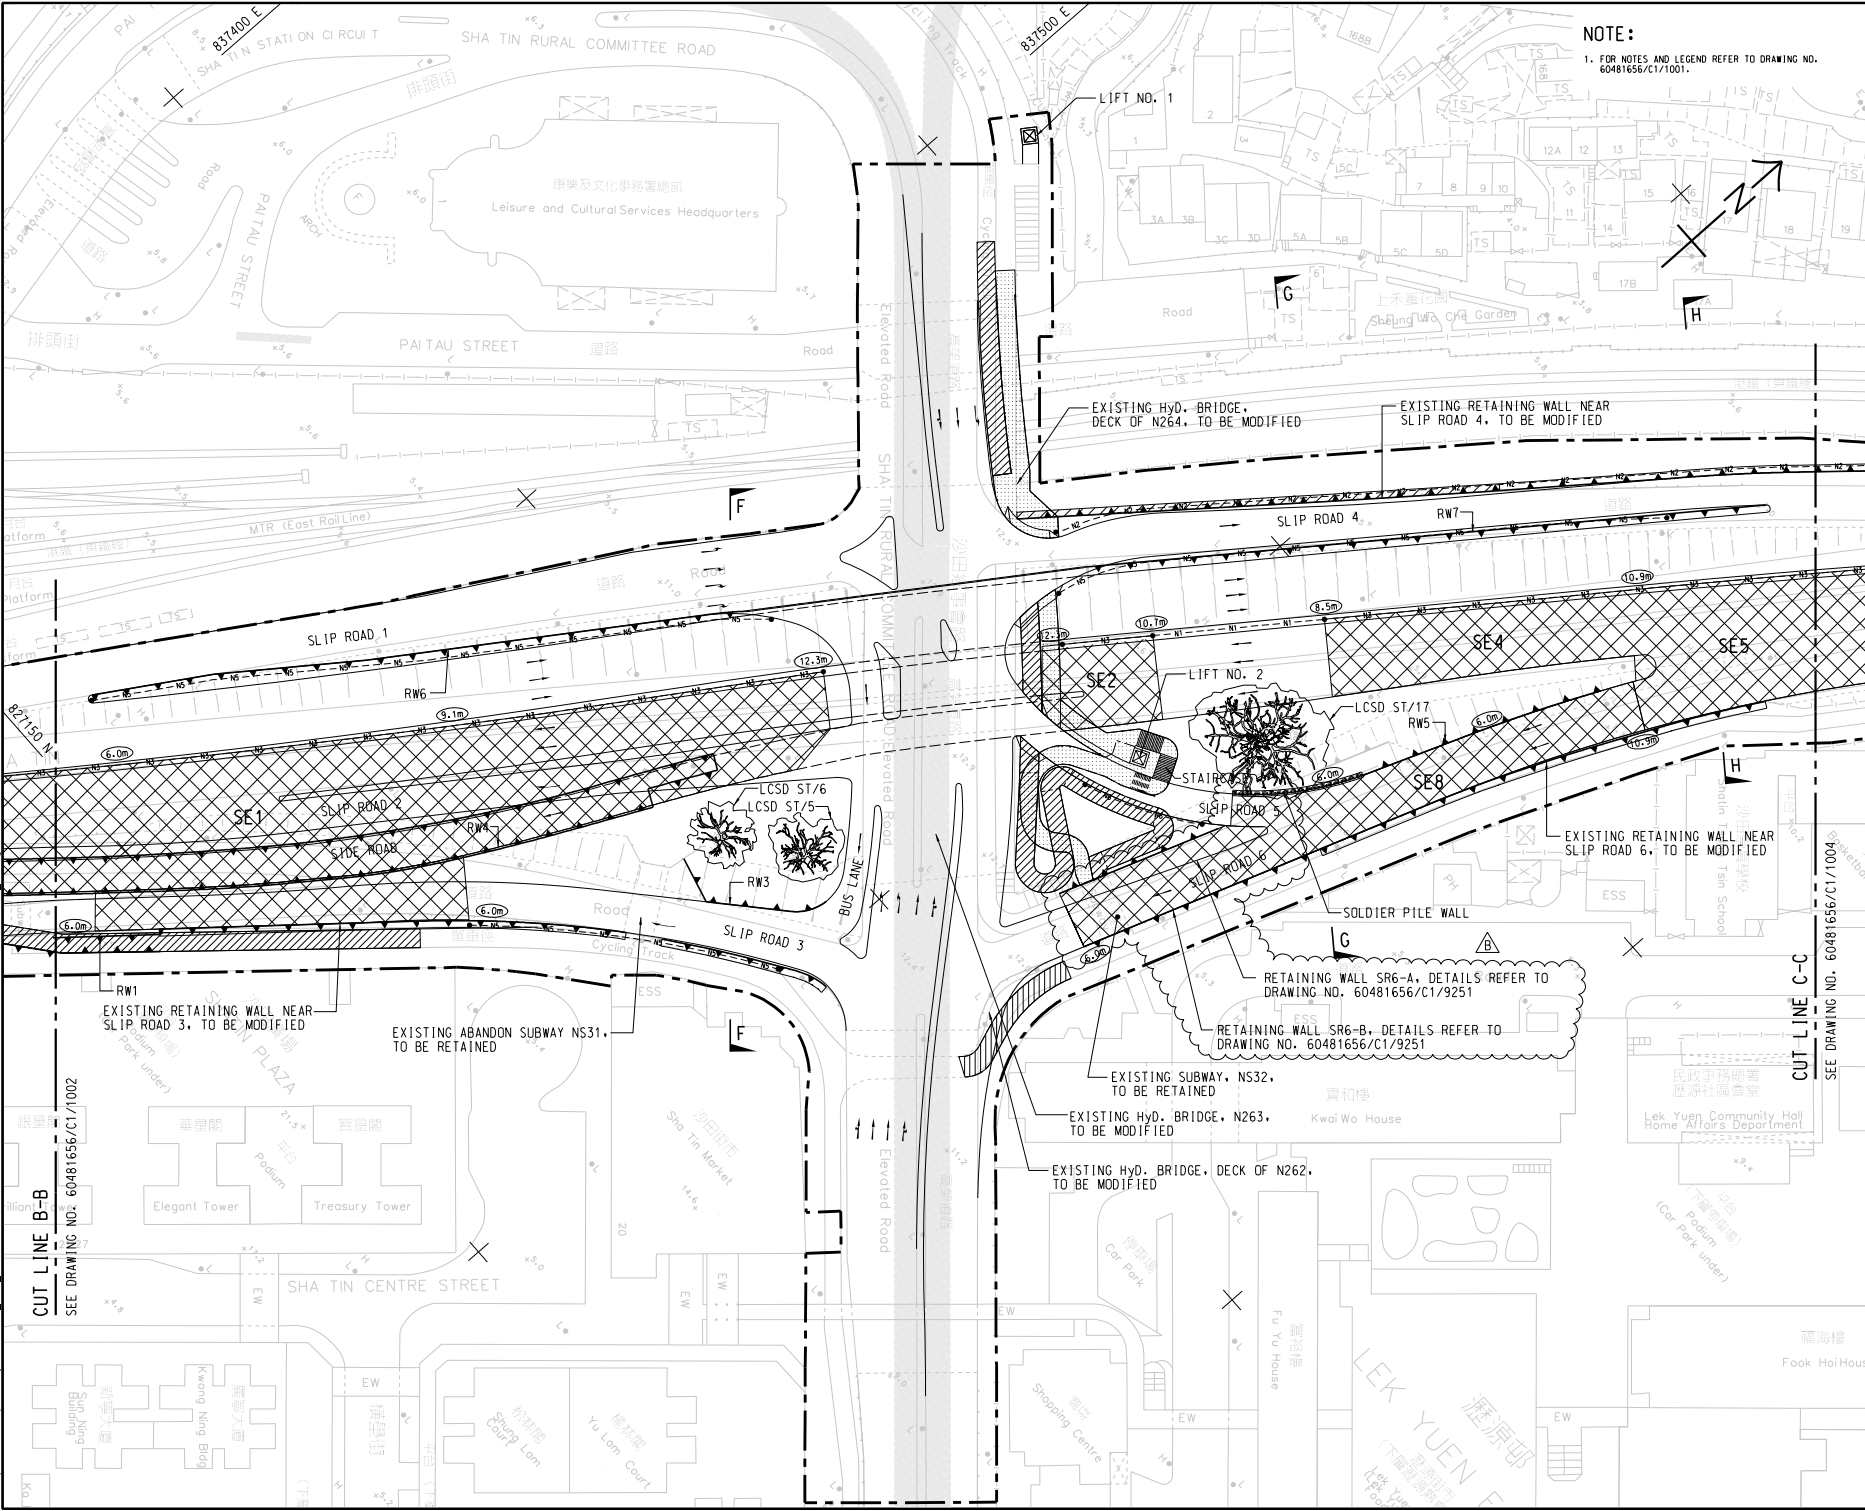

AECOM

PROJECT
60481656/C1/1001

ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
Civil Engineering and Development Department

CONSULTANT
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

ISSUE/REVISION

REV	DATE	DESCRIPTION	CHK
B	FEB. 18	TENDER ADDENDUM NO. 2	BCC
A	FEB. 18	TENDER ADDENDUM NO. 1	BCC
-	JAN. 18	TENDER DRAWING	BCC

STATUS

SCALE
A1: 1:500
DIMENSION UNIT
METRES

KEY PLAN
A1: 1:40000


CONTRACT NO.
NE/2017/05

SHEET TITLE
GENERAL LAYOUT PLAN
FIGURE 1,1 b

SHEET NUMBER
60481656/C1/1003B

SHEET 3 OF 6

15/01/2018 11:15:10
 P:\1\151218\AS\W\MT\DW\H\KST\TAIPO\66-ASCOM\AECOM_DS02_AS\Documents\60481656\WTP-STCAB-PRODUCTION\DRAWING\CONTRACT\11000\11000-C1-1004.dgn
 Project Management: Helmut
 Designer: F.H.S.C. Cheuk-wai BCC
 Approved: C.W.N.
 C.W.N.
 ISO A1 842mm x 841mm

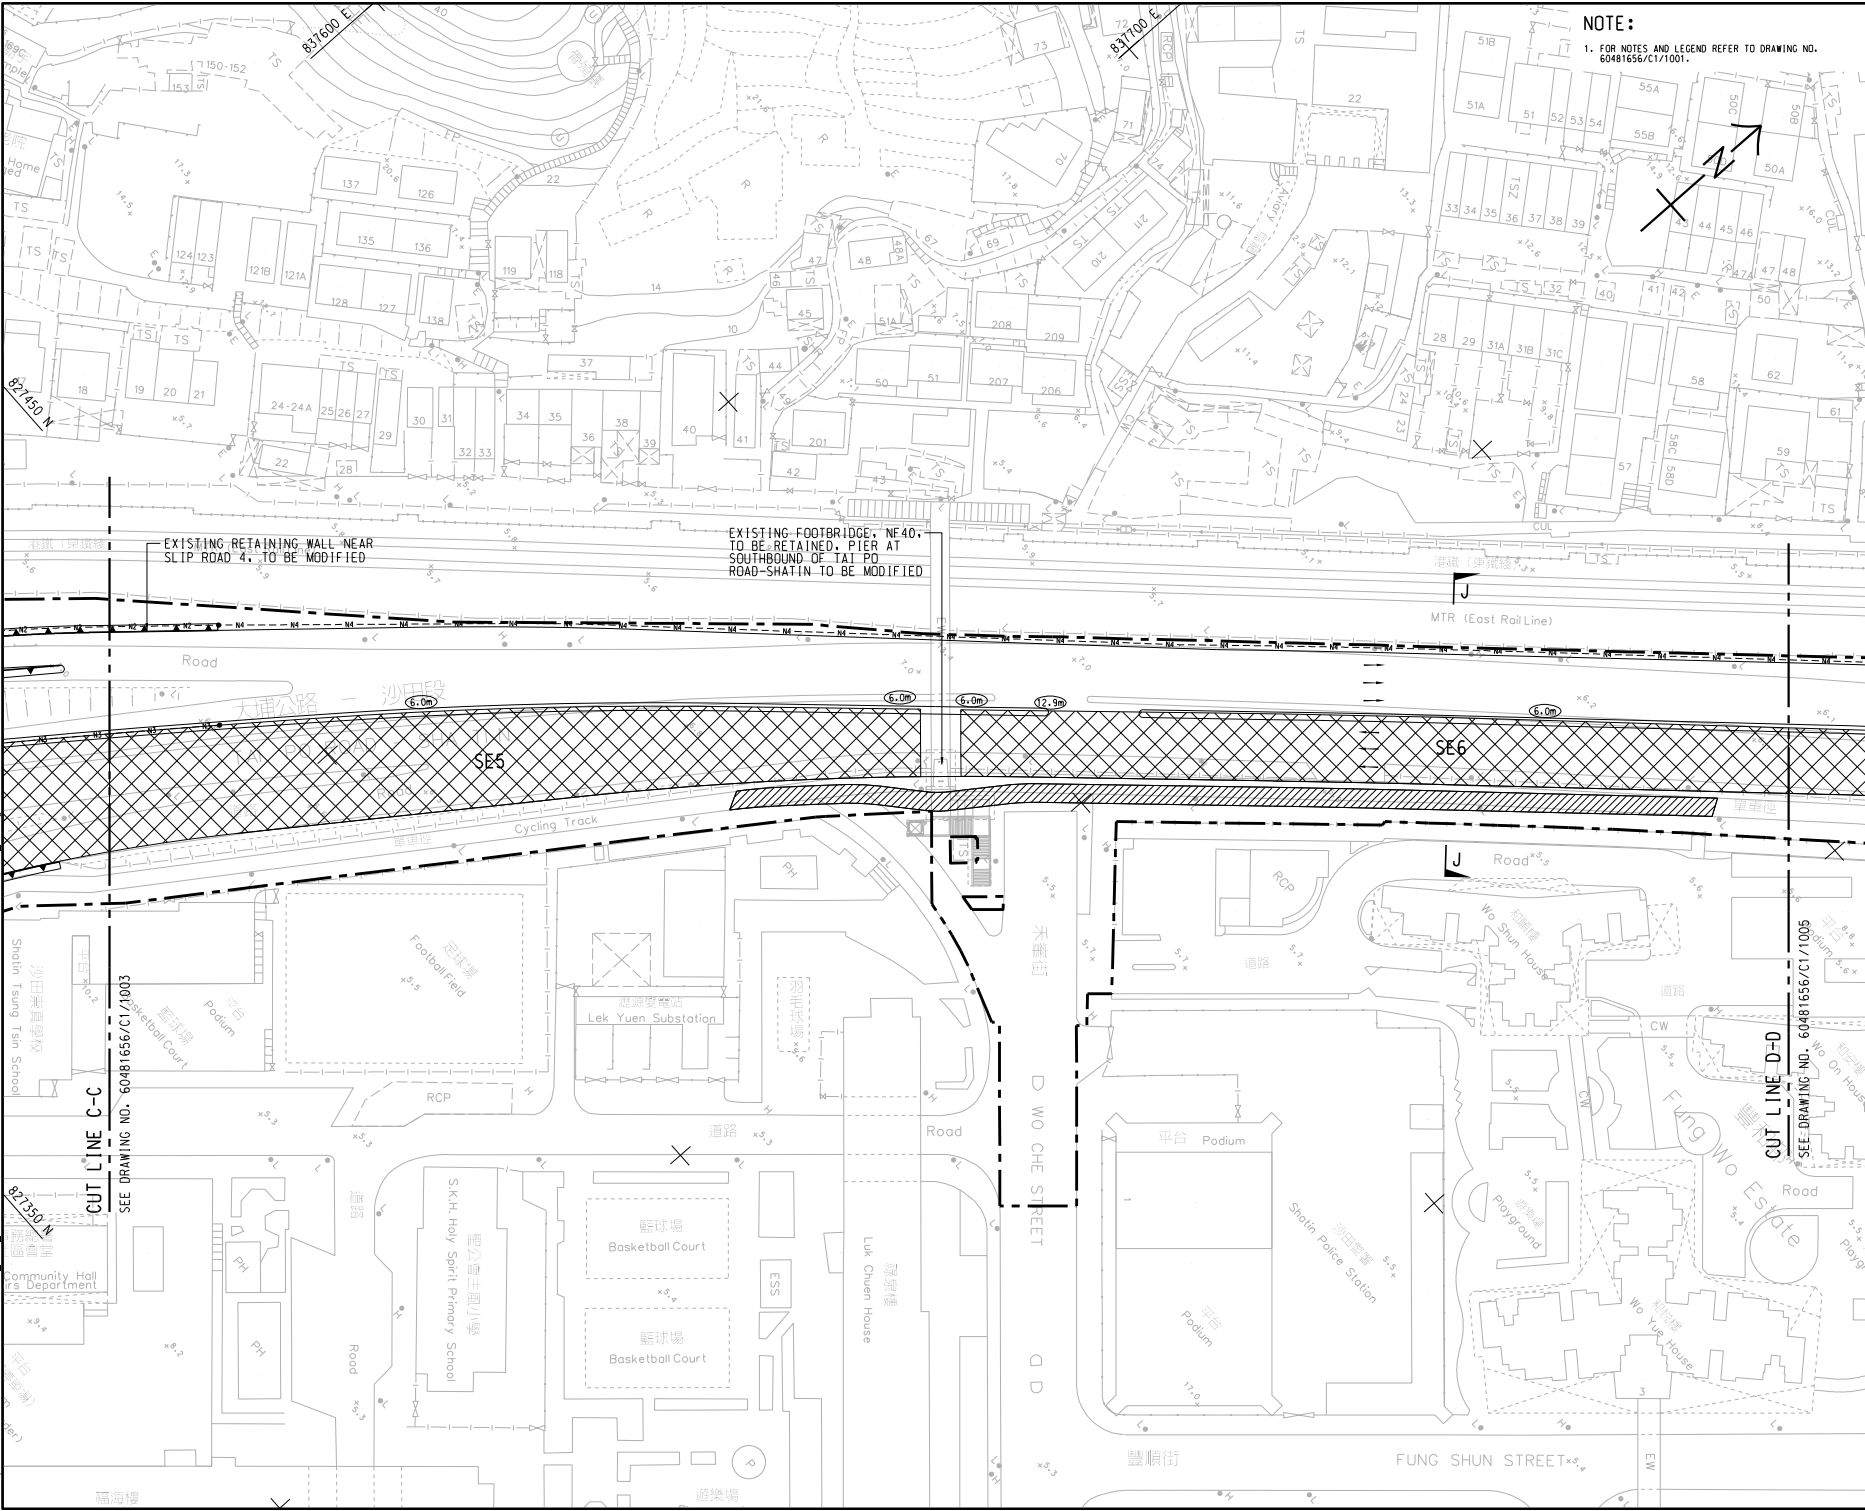

NOTE:
 1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/C1/1001.

AECOM

PROJECT
 ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
 Civil Engineering and Development Department

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS
 沙利工程顧問公司

ISSUE/REVISION

IR	DATE	DESCRIPTION	CHK.
-	JAN. 18	TENDER DRAWING	BCC
1/1			
2/1			
3/1			
4/1			
5/1			
6/1			
7/1			
8/1			
9/1			
10/1			

STATUS

SCALE
 A1: 1:500
 DIMENSION UNIT
 METRES

KEY PLAN
 A1: 1:40000

CONTRACT NO.
 NE/2017/05


SHEET TITLE
 GENERAL LAYOUT PLAN
 FIGURE 1.1b

SHEET NUMBER
 60481656/C1/1004

SHEET 4 OF 6

This drawing has been prepared for the use of AECOM and its staff, and is not to be used, modified, reproduced or distributed by third parties without the prior written approval of AECOM. AECOM accepts no responsibility for any errors or omissions in this drawing, and no liability for any loss or damage caused by its use. All measurements shall be taken from the master drawings.

19/12/2018
 PLOT FILE BY: XE/EP
 DATL: jerry.koh@hstt.com.hk
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN
 IBO A1 84mm x 64mm
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN
 14/12/2018
 PLOT FILE BY: XE/EP
 DATL: jerry.koh@hstt.com.hk
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN

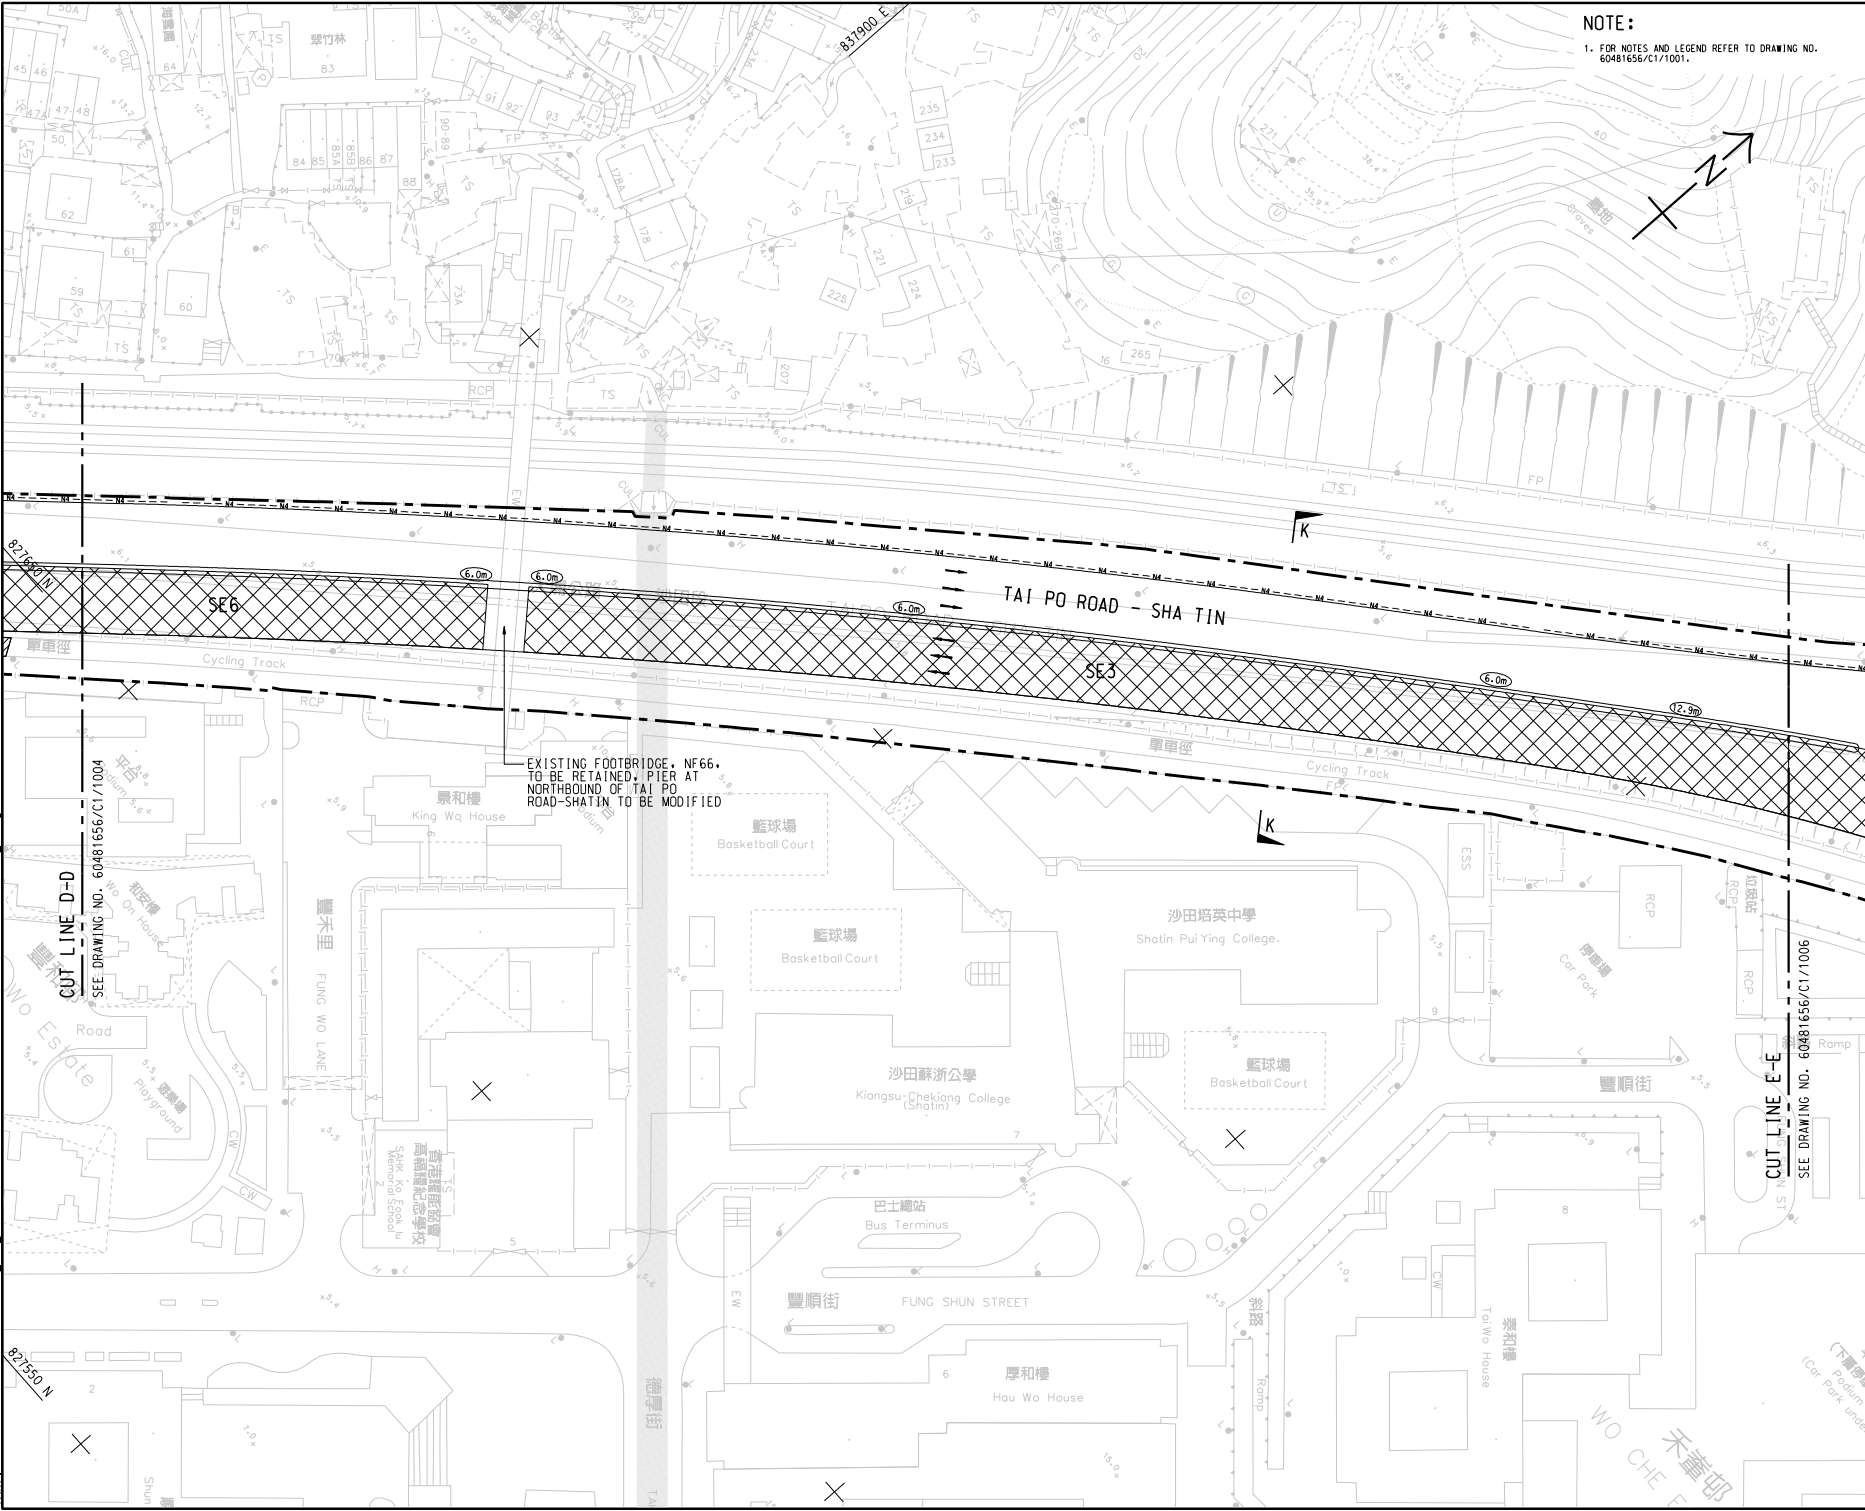

NOTE:
 1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/C1/1001.

AECOM

PROJECT
ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
 Civil Engineering and Development Department


CONSULTANT
AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK	APP
1	JAN 18	TENDER DRAWING	BCC	

SCALE
 A1: 1:500
 DIMENSION UNIT
 METRES




CONTRACT NO.
 NE/2017/05

SHEET TITLE
 GENERAL LAYOUT PLAN
 FIGURE 1.1b

SHEET NUMBER
 60481656/C1/1005

SHEET 5 OF 6

Project Management: HHLHK; Designer: FNSC; Checked: BCC; Approved: CWN; BSO A1 84mm x 84mm; 22/2018; PE1 TAU VILLAGE; AECOM; SITE; STACAD; PRODUCTION; DRAWING; CONTRACT; 11000/C1_1006.6p; PE1 TAU VILLAGE; AECOM; SITE; STACAD; PRODUCTION; DRAWING; CONTRACT; 11000/C1_1006.6p; PE1 TAU VILLAGE; AECOM; SITE; STACAD; PRODUCTION; DRAWING; CONTRACT; 11000/C1_1006.6p; PE1 TAU VILLAGE; AECOM; SITE; STACAD; PRODUCTION; DRAWING; CONTRACT; 11000/C1_1006.6p

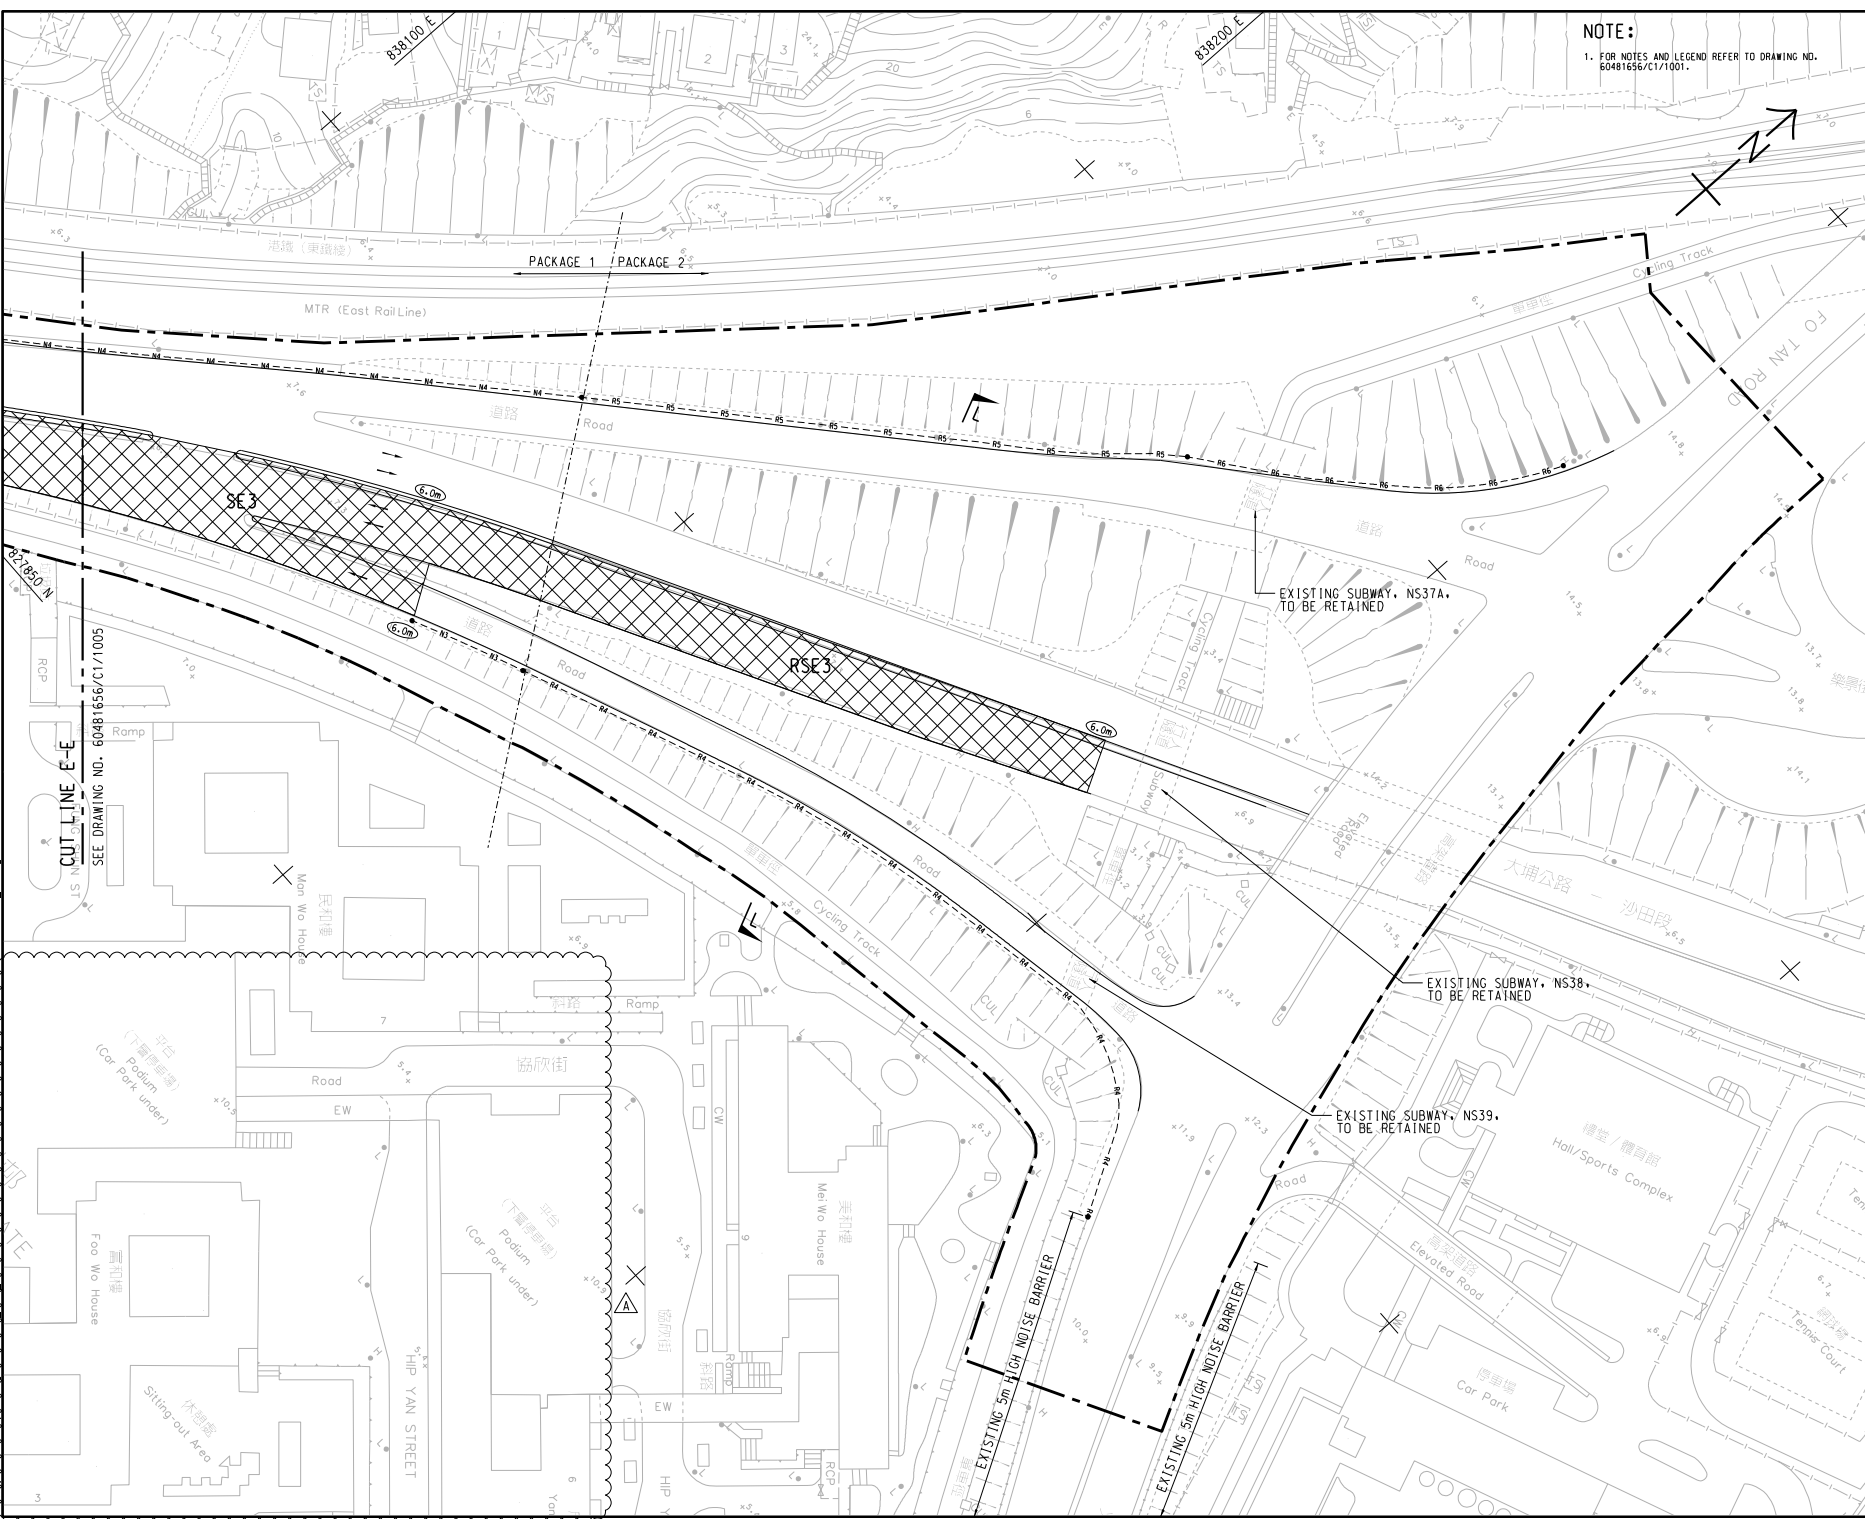

NOTE:
1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/C1/1001.

AECOM

PROJECT
ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
Civil Engineering and Development Department


CONSULTANT
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
沙利工程顧問公司

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	FEB, 18	TENDER ADDENDUM NO.2	BCC
B	JAN, 18	TENDER DRAWING	BCC
DR	DATE	DESCRIPTION	CHK.

STATUS
SCALE: A1 1:500; DIMENSION UNIT: METRES
KEY PLAN: A1 1:40000



CONTRACT NO. NE/2017/05

SHEET TITLE
GENERAL LAYOUT PLAN
FIGURE 1.1b

SHEET NUMBER
60481656/C1/1006A

SHEET 6 OF 6

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 2a

Air Monitoring Locations

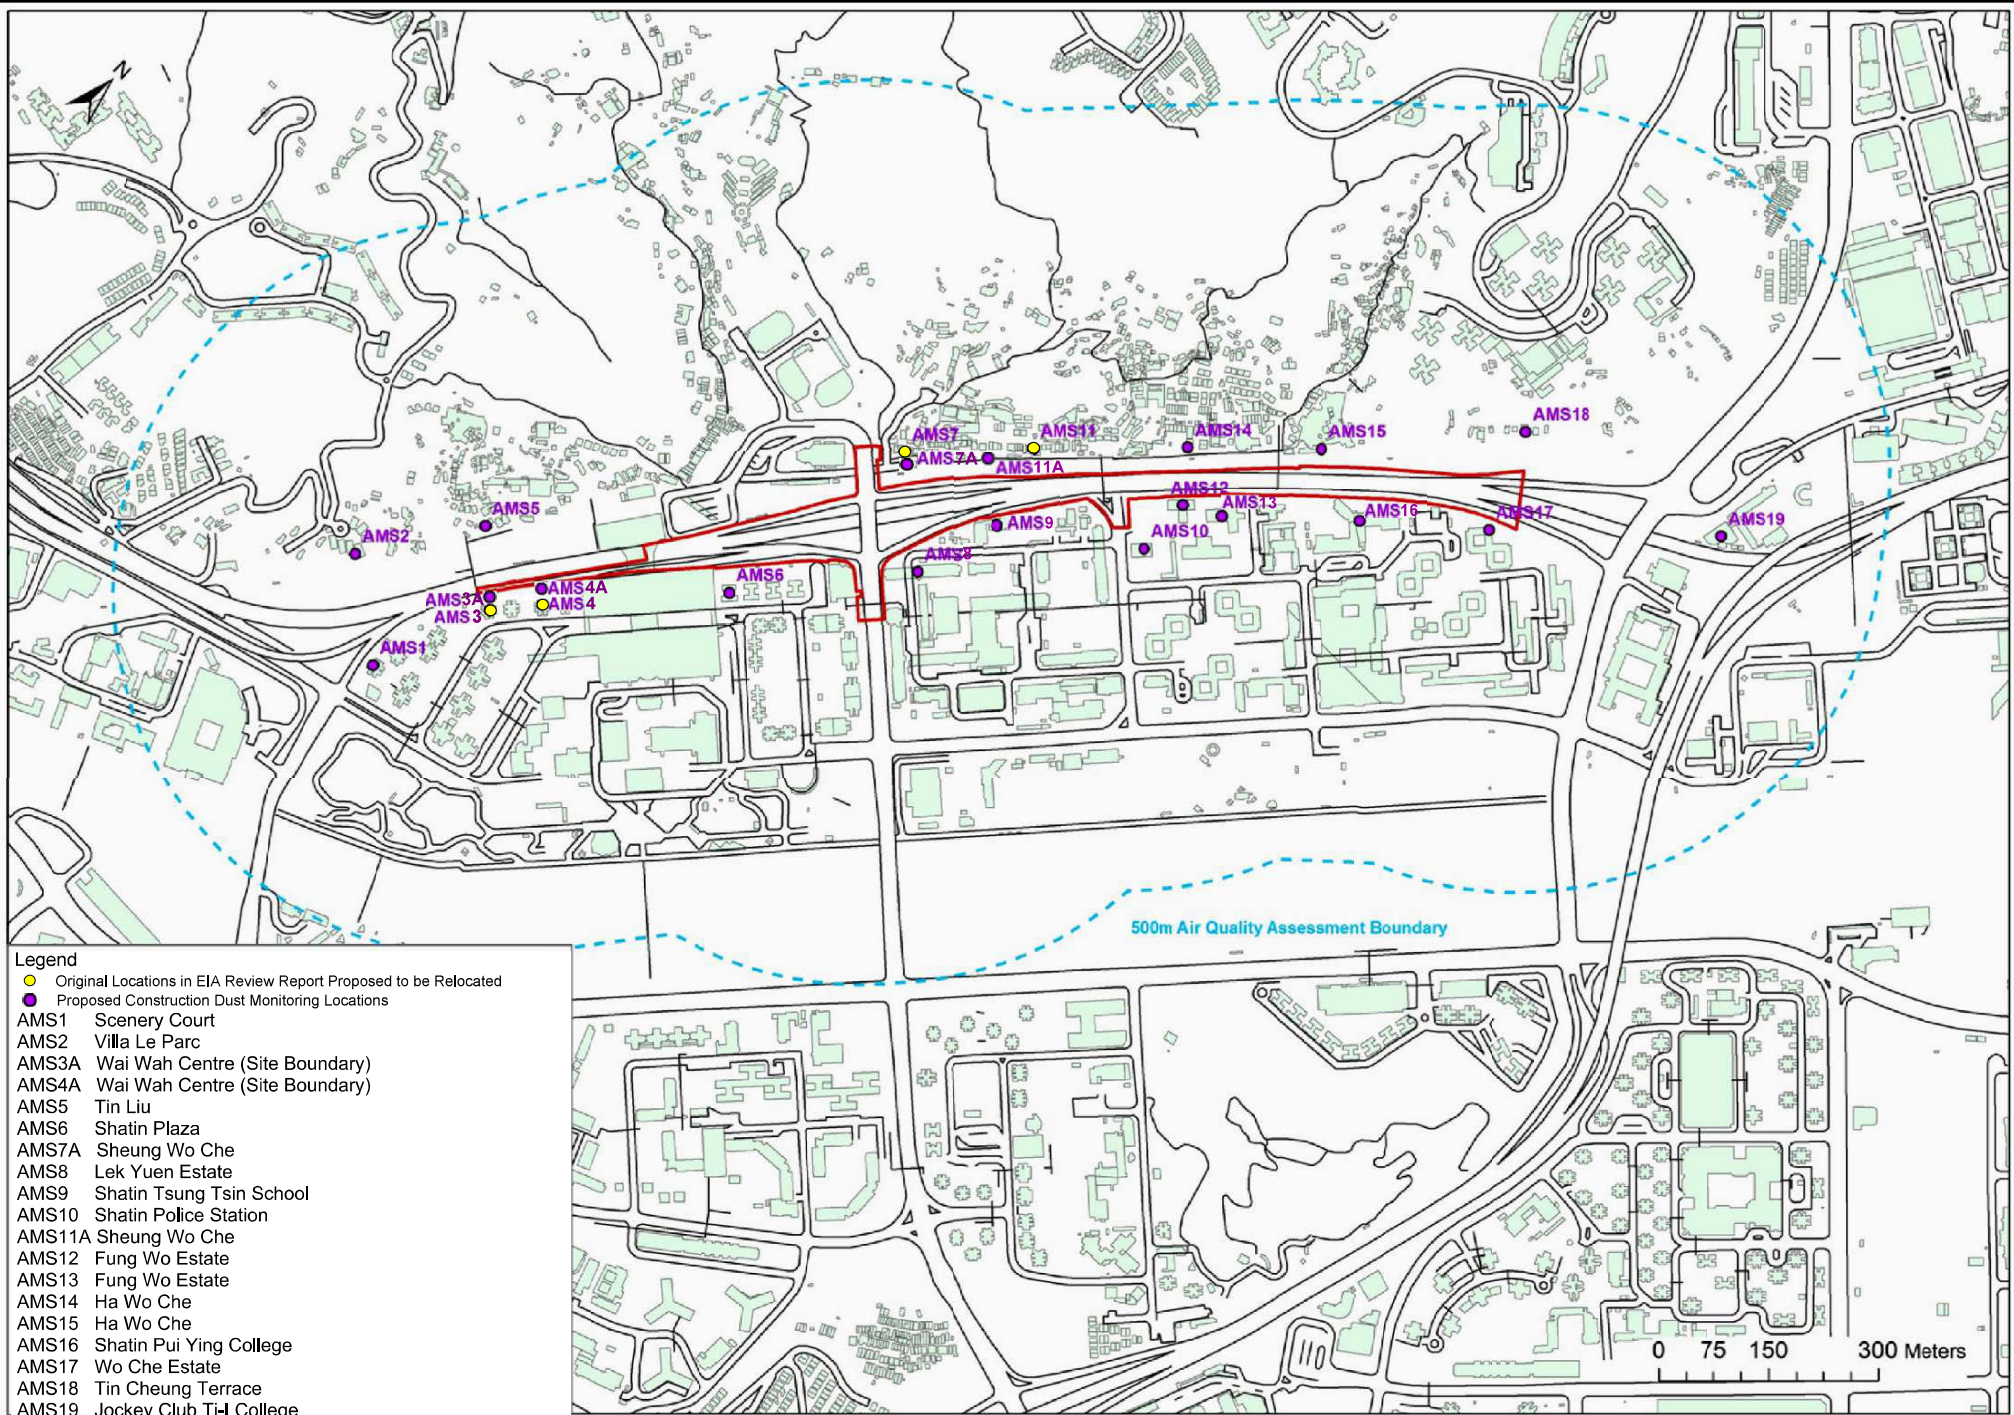


Figure 2a Air Quality Monitoring Locations

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 2b

Noise Monitoring Locations

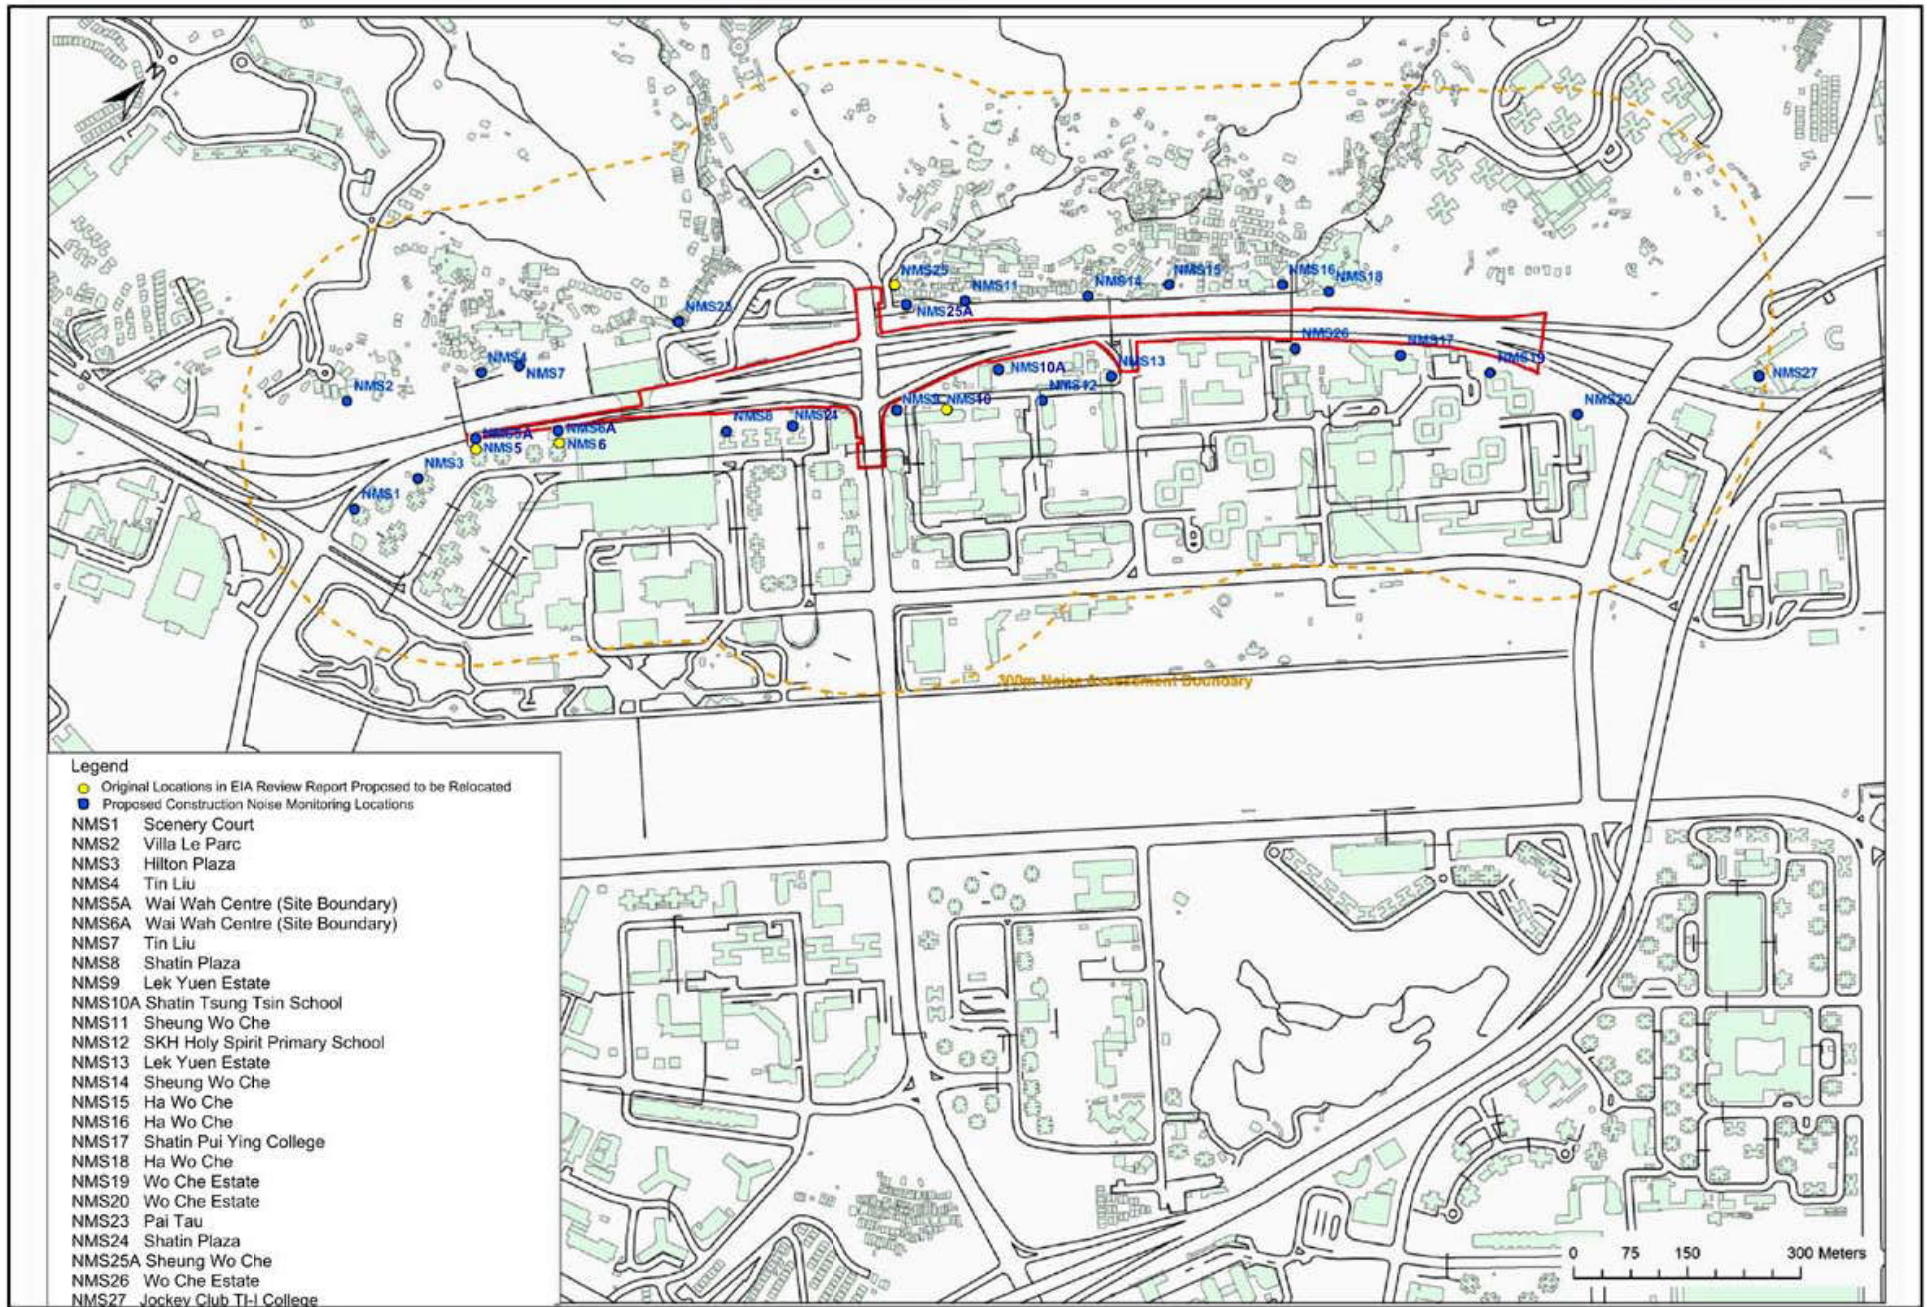


Figure 2b Noise Monitoring Locations

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix A


Construction Programme

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP11 Start	AP11 Finish	2021					
								Sep 39	Oct 40	Nov 41	Dec 42	2022 Jan 43	
Contract NE/2017/05 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)													
PROJECT KEY DATES													
PROJECT COMPLETION													
KEY1130	Contract Completion of Section 3	0	0		18-Oct-21*		18-Oct-21						
PRELIMINARIES & GENERAL REQUIREMENT													
GENERAL SUBMISSION													
SUB1403	ITP's for Lighting Luminaires and System	0	0	30-Sep-21*		30-Apr-21							
SUB1405	All Lighting Designs	0	0	30-Sep-21*		30-Apr-21							
SUB1410	Combined Services Drawings (CSD)	0	0	30-Sep-21*		30-Apr-21							
DESIGN SUBMISSION													
NOISE MITIGATION MEASURES													
DES1260	Re-submit Foundation Design of Noise Mitigation Measures in Zone 3 w/Design Certificate	23	12	29-Mar-21 A	11-Oct-21	31-Mar-21	22-Apr-21						
DES1270	PM Consent for Construction	28	28	11-Oct-21	08-Nov-21	11-May-21	08-Jun-21						
DES1290	PM review & comment	28	11	07-Aug-19 A	11-Oct-21	31-Aug-19	27-Sep-19						
DES1300	Re-submit Superstructure Design of Noise Mitigation Measures in Zone 1 & 2 w/Design Certificate	20	20	12-Oct-21	01-Nov-21	12-May-21	01-Jun-21						
DES1310	PM Consent for Construction	28	28	01-Nov-21	29-Nov-21	01-Jun-21	29-Jun-21						
DES1330	PM review & comment	28	11	07-Aug-19 A	11-Oct-21	31-Aug-19	27-Sep-19						
DES1340	Re-submit Superstructure Design of Noise Mitigation Measures in Zone 3 w/Design Certificate	21	21	12-Oct-21	02-Nov-21	12-May-21	02-Jun-21						
DES1350	PM Consent for Construction	28	28	02-Nov-21	30-Nov-21	02-Jun-21	30-Jun-21						
DES1370	PM review & comment	28	11	07-Aug-19 A	11-Oct-21	31-Aug-19	27-Sep-19						
DES1380	Re-submit Superstructure Design of Noise Mitigation Measures in Zones 4 & 5 w/Design Certificate	20	20	12-Oct-21	01-Nov-21	12-May-21	01-Jun-21						
DES1390	PM Consent for Construction	28	28	01-Nov-21	29-Nov-21	01-Jun-21	29-Jun-21						
REMAINING WORKS													
DES1490	PM review & comment	28	1	25-Jan-19 A	30-Sep-21	04-Aug-19	01-Sep-19						
DES1500	Re-submit Foundation Design of Pedestrian Lift 1 & 2, Lift 2 Staircase, Cycle Track Ramp & Sign Gantry w/Design Certificate	35	1	13-Apr-20 A	02-Oct-21	02-Jun-20	07-Jul-20						
DES1510	PM Consent for Construction	28	28	02-Oct-21	30-Oct-21	02-May-21	30-May-21						
DES1530	PM review & comment	28	1	02-Jan-19 A	30-Sep-21	31-Jan-19	27-Feb-19						
DES1540	Re-submit Design of Watermain & Irrigation System w/Design Certificate	32	1	02-Jan-19 A	30-Sep-21	02-Apr-19	03-May-19						
DES1560	Prepare & submit Design of E&M System (E&M & Road Lighting) w/Design Certificate	35	35	30-Sep-21	03-Nov-21	30-Apr-21	03-Jun-21						
DES1570	PM review & comment	28	28	04-Nov-21	01-Dec-21	04-Jun-21	01-Jul-21						
DES1580	Re-submit Design of E&M System (E&M & Road Lighting) w/Design Certificate	32	32	03-Dec-21	03-Jan-22	03-Jul-21	03-Aug-21						
DES1590	PM Consent for Construction	28	28	04-Jan-22	31-Jan-22	04-Aug-21	31-Aug-21						
SUBLETTING & PROCUREMENT SCHEDULE													
SUBLETTING													
SPS1180	Flexible Surfacing	30	15	31-Oct-20 A	22-Oct-21	13-Jul-21	11-Aug-21						
SPS1190	Road Marking and Road Studs	30	23	30-Nov-20 A	22-Oct-21	13-Jul-21	11-Aug-21						
SPS1210	Drainage (PC pipe, manhole & gully) and Duct	30	5	31-Mar-20 A	04-Oct-21	01-May-21	30-May-21						
SPS1230	Sub-base and Concrete pavement	30	15	31-Oct-20 A	22-Oct-21	12-May-21	11-Jun-21						
SPS1440	Drainage for Noise Mitigation Measures	30	5	31-Mar-20 A	04-Oct-21	30-Apr-21	29-May-21						

XXXX Remaining Level of Effort
 Remaining Work
 ◆ Milestone
 ◆ Baseline Milestone
 Actual Level of Effort
 Critical Remaining Work
◆
 Primary Baseline
 Actual Work


ROAD WIDENING & RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)
3 Months Rolling Programme (30/9/21)
 Page 1 of 7

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

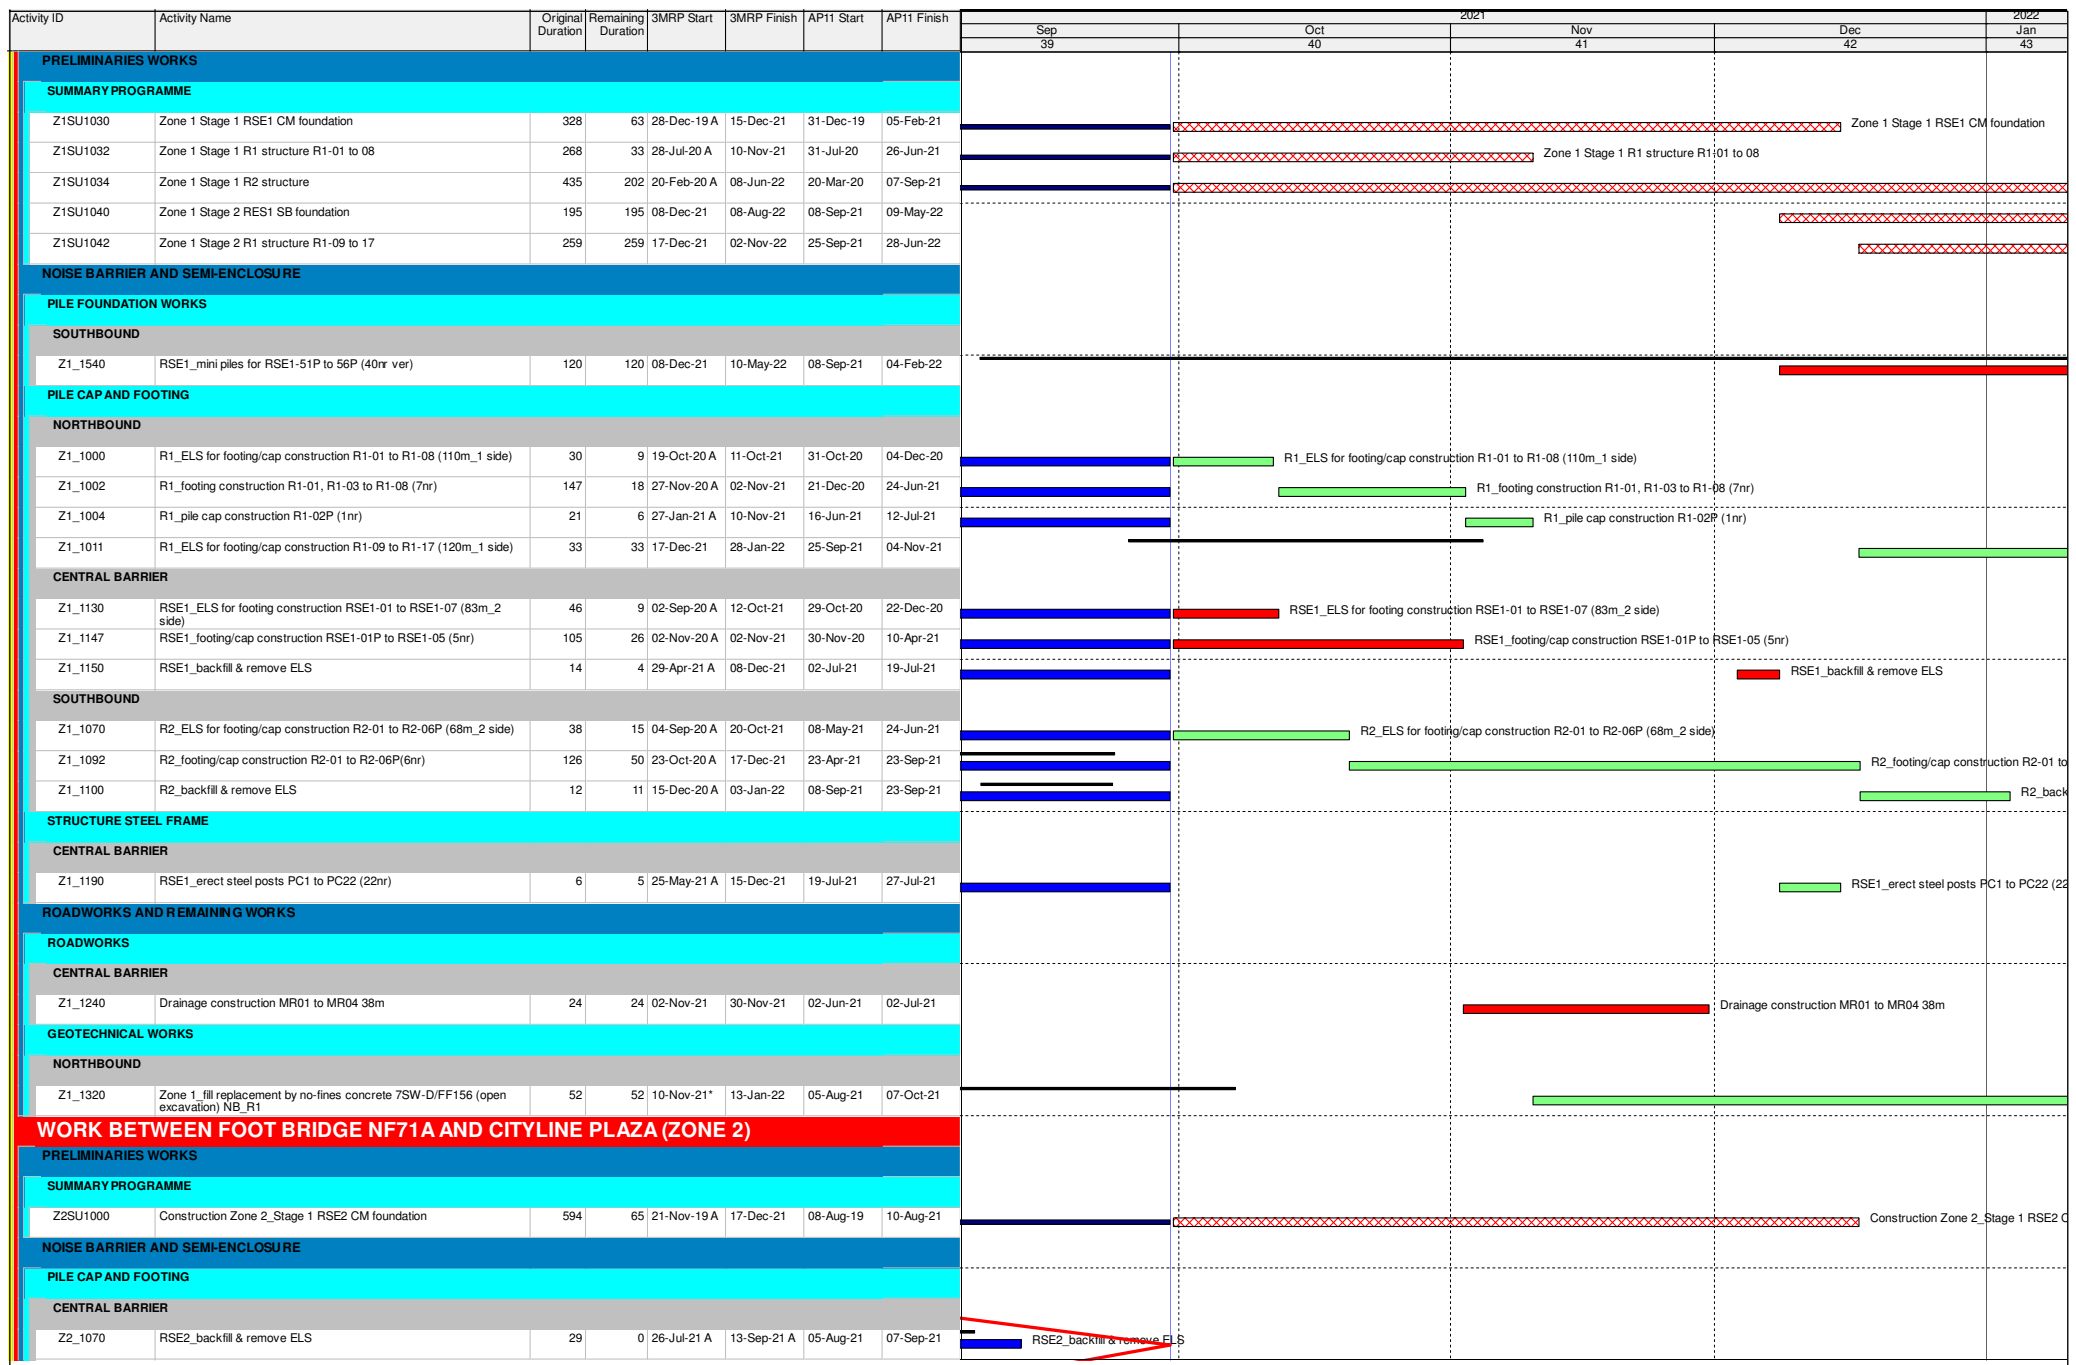

- Remaining Level of Effort
- Remaining Work
- Milestone
- Actual Level of Effort
- Critical Remaining Work
- Baseline Milestone
- Actual Work
- Primary Baseline

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

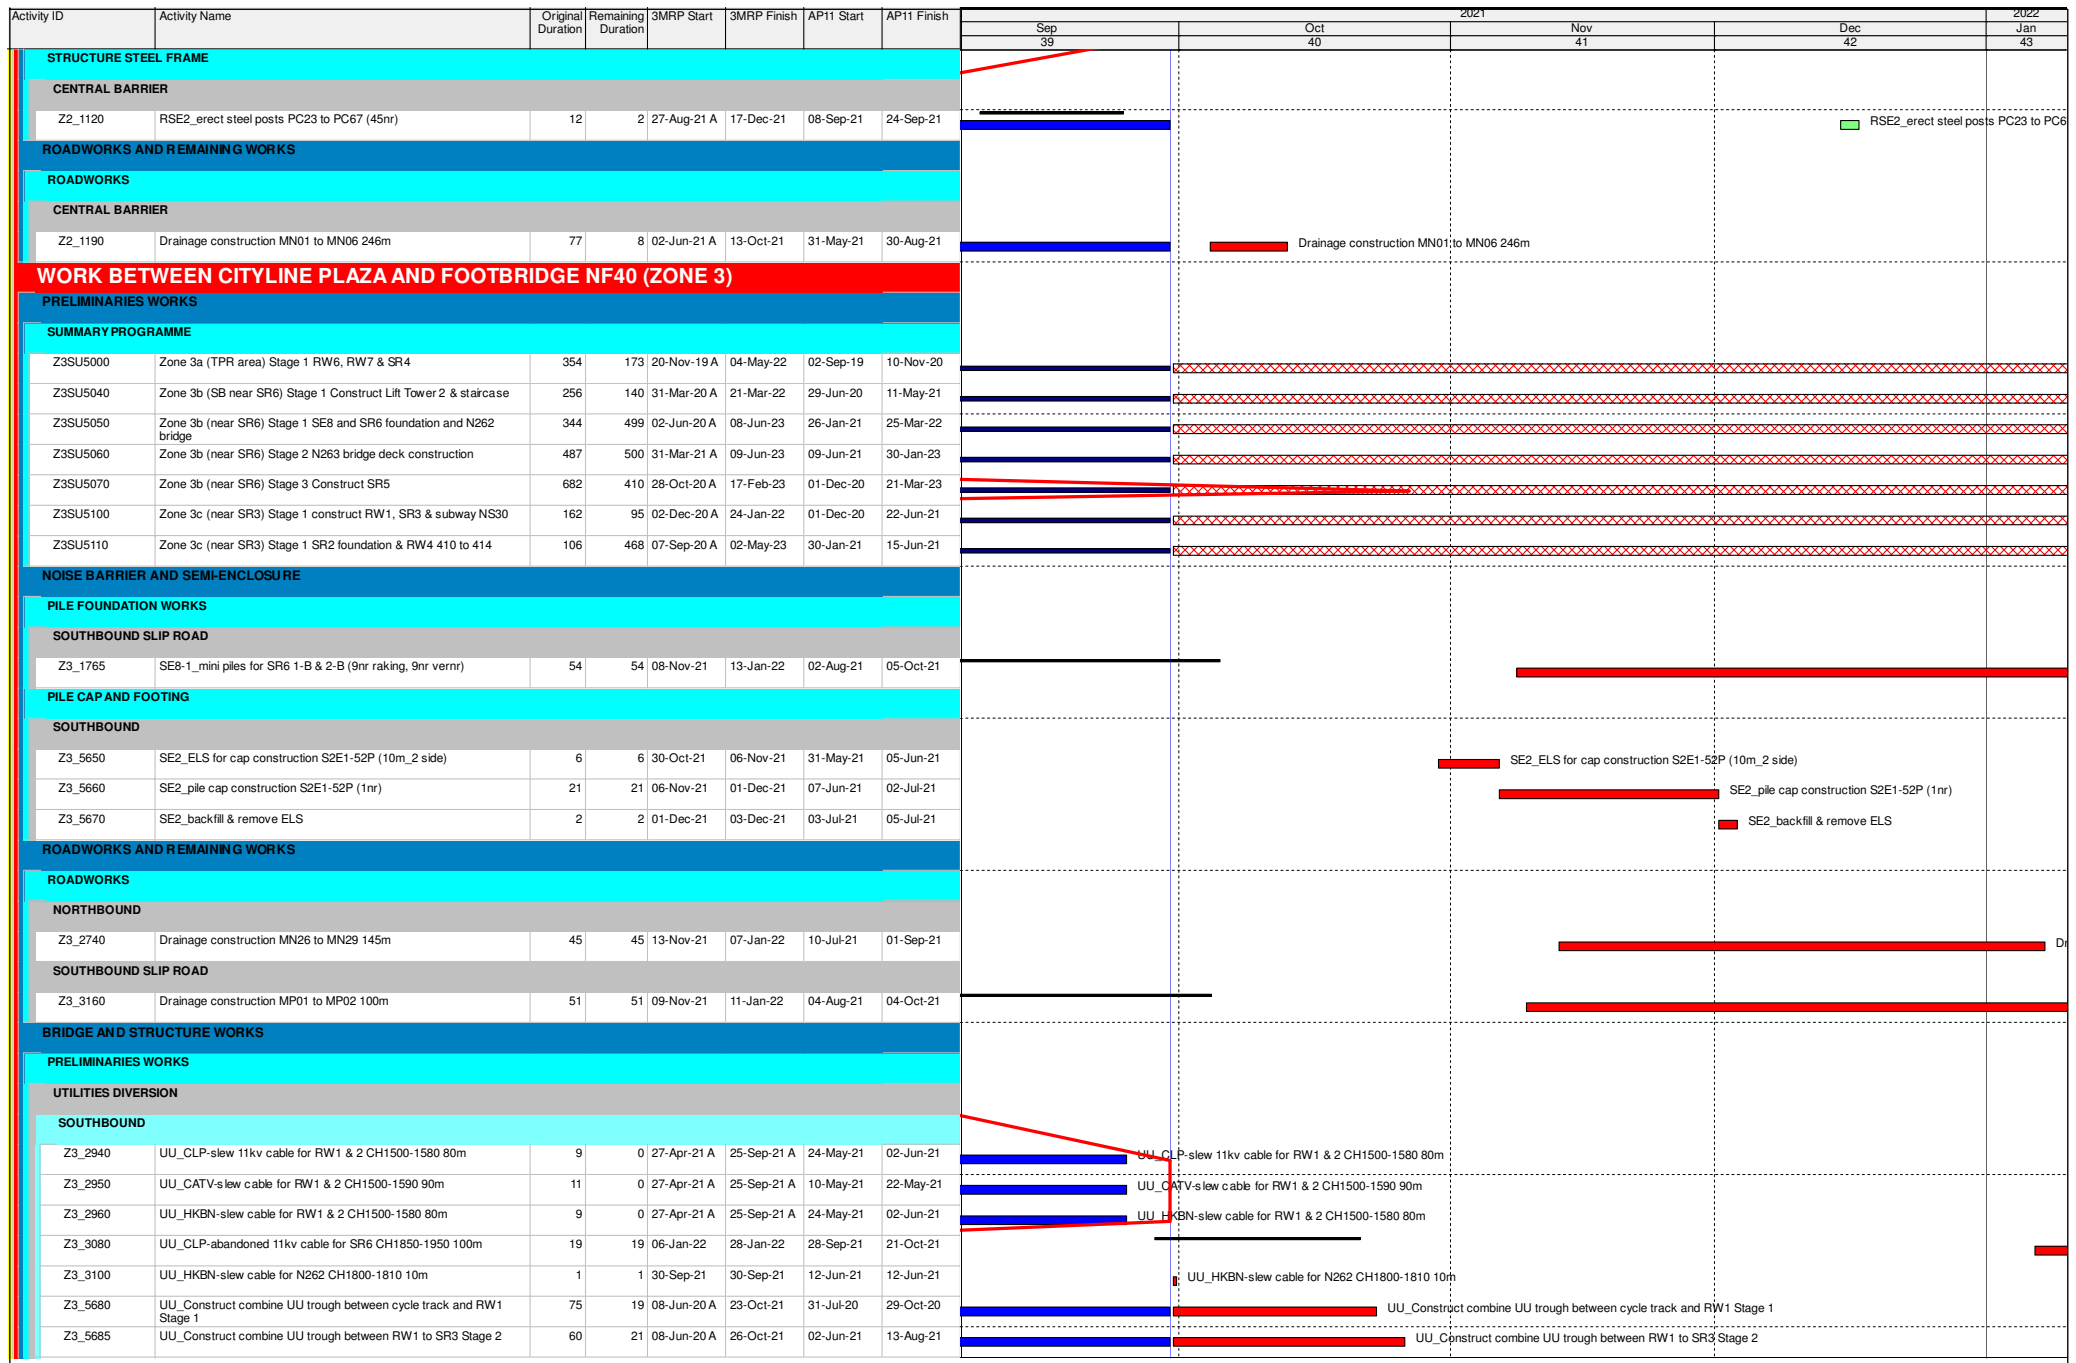

- Remaining Level of Effort
- Remaining Work
- Milestone
- Critical Remaining Work
- Actual Level of Effort
- Actual Work
- Primary Baseline
- Baseline Milestone

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP11 Start	AP11 Finish	2021							
								Sep 39	Oct 40	Nov 41	Dec 42	2022 Jan 43			
WIDENING FOR NORTH HOLLOW ABUTMENT (N264)															
Z3_4210	C01_column construction	28	28	28-Dec-21	31-Jan-22	31-Jul-21	02-Sep-21								
Z3_4240	N264_temporary protection MTRC cable	42	42	28-Dec-21	19-Feb-22	31-Jul-21	18-Sep-21								
MODIFICATION OF BRIDGE N263															
RECONSTRUCTION ABUTMENT WALL AT NHA															
Z3_4140	NAW-1_ELS, excavation & pile cap construction	60	24	23-Oct-20 A	29-Oct-21	30-Nov-20	10-Feb-21								
Z3_4142	Demolish part of existing North Hollow Abutment wall for construction new wall	45	27	22-Apr-21 A	02-Nov-21	30-Apr-21	24-Jun-21								
Z3_4190	NAW_construct new abutment wall (North side)	60	54	25-May-21 A	03-Dec-21	31-May-21	11-Aug-21								
Z3_4195	NAW_construct new abutment wall (Remaining)	75	75	03-Nov-21	04-Feb-22	02-Jul-21	28-Sep-21								
MODIFICATION EXISTING SOUTH HOLLOW ABUTMENT WALL															
Z3_3950	SHA_piling works for pier SHA6 nos. Socket H-pile	48	48	30-Sep-21*	27-Nov-21	06-Sep-21	04-Nov-21								
Z3_3960	SHA_ELS & pile cap construction	45	45	27-Nov-21	22-Jan-22	04-Nov-21	29-Dec-21								
DECK CONSTRUCTION OF BRIDGE N263															
Z3_3880	N263_erec temporary working platform for deck construction (widen Area)	35	0	31-Mar-21 A	24-Sep-21 A	09-Jun-21	01-Sep-21								
Z3_3980	Construct the widen deck area PB-128a/b to 132a/b (Stage 1)	75	75	28-Dec-21	29-Mar-22	01-Sep-21	01-Dec-21								
NEW SLIP ROAD 2															
Z3_5350	SR2-1_ELS & pile cap construction	30	29	28-Sep-21 A	05-Nov-21	01-Jun-21	07-Jul-21								
Z3_5416	SR2-2A/B_ELS & pile cap construction	30	30	05-Nov-21	10-Dec-21	08-Jul-21	11-Aug-21								
LIFT TOWER 1															
Z3_3600	L1-PC1_piling works 4nr socket H-pile	32	32	30-Oct-21*	07-Dec-21	06-Sep-21	16-Oct-21								
Z3_3610	L1-PC1_ELS & pile cap construction	60	60	07-Dec-21	22-Feb-22	16-Oct-21	28-Dec-21								
LIFT TOWER 2 & STAIRCASE															
Z3_3690	Lift Tower 2_erec steel structure	28	28	30-Oct-21*	02-Dec-21	02-Jul-21	03-Aug-21								
Z3_3700	Lift Tower 2_external finishing	45	45	02-Dec-21	27-Jan-22	04-Aug-21	25-Sep-21								
Z3_3710	Lift Tower 2_lift instalation	75	75	02-Dec-21	07-Mar-22	04-Aug-21	02-Nov-21								
Z3_3802	Lift Tower 2_Pier 2 column construction	21	21	03-Dec-21	30-Dec-21	30-Jul-21	23-Aug-21								
Z3_3804	Lift Tower 2_Pier 1 column construction	21	21	03-Dec-21	30-Dec-21	30-Jul-21	23-Aug-21								
Z3_3820	Staircase_staircase construction between Pier 3 and Pier 2	30	30	30-Dec-21	08-Feb-22	24-Aug-21	28-Sep-21								
Z3_3830	Staircase_bridge deck construction between Pier 2 and Pier 1	30	30	30-Dec-21	08-Feb-22	24-Aug-21	28-Sep-21								
NEW SLIP ROAD 5															
Z3_5490	SR5-3_piling works 21nr mini pile	84	75	25-Aug-21 A	31-Dec-21	21-Jun-21	28-Sep-21								
Z3_5500	SR5-3_ELS & pile cap construction	35	35	31-Dec-21	15-Feb-22	29-Sep-21	10-Nov-21								
Z3_5540	SR5-2_ELS & pile cap construction	45	45	31-Dec-21	26-Feb-22	29-Sep-21	22-Nov-21								
RETAINING WALL & SUBWAY															
RETAINING WALL NO.1															
Z3_4555	RW1_Diversion existing CLP cable	14	14	30-Sep-21*	18-Oct-21	17-May-21	02-Jun-21								
Z3_4560	RW1_ELS works for Bay 101 to Bay 104 (56m_2 side)	31	6	22-May-21 A	03-Nov-21	03-Jun-21	10-Jul-21								
Z3_4570	RW1_base slab construction for Bay 101 to Bay 104	32	8	25-May-21 A	04-Nov-21	23-Jun-21	30-Jul-21								
Z3_4580	RW1_retaining wall construction for Bay 101 to Bay 104	40	10	04-Jun-21 A	23-Nov-21	13-Jul-21	27-Aug-21								
Z3_4590	RW1_remove ELS & backfill for Bay 101 to Bay 104	10	10	29-Dec-21	11-Jan-22	22-Sep-21	04-Oct-21								
Z3_4600	RW1_demolish existing retaining structure between Bay 105 and Bay 107	45	14	02-Jul-21 A	26-Oct-21	30-Apr-21	24-Jun-21								
Z3_4610	RW1_ELS works for Bay 105 to Bay 107 (29m_2 side)	16	11	26-Feb-21 A	15-Nov-21	12-Jul-21	29-Jul-21								
Z3_4620	RW1_base slab construction for Bay 105 to Bay 107	24	16	14-Aug-21 A	03-Dec-21	31-Jul-21	27-Aug-21								

- Remaining Level of Effort
- Remaining Work
- ◆ Milestone
- ◆ Baseline Milestone
- Actual Level of Effort
- Critical Remaining Work
- ◆ Baseline Milestone
- Actual Work
- Primary Baseline

ROAD WIDENING & RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)
3 Months Rolling Programme (30/9/21)
Page 4 of 7

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP11 Start	AP11 Finish	2021					2022
								Sep 30	Oct 31	Nov 30	Dec 31	Jan 31	
Z3_4630	RW1_retaining wall construction for Bay 105 to Bay 107	30	30	03-Dec-21	11-Jan-22	28-Aug-21	04-Oct-21						
RETAINING WALL NO.6													
Z3_1218_1020	RW6_retaining wall construction for Bay 601 to Bay 606	72	36	11-Mar-21 A	12-Nov-21	31-Mar-21	30-Jun-21						
Z3_1218_1030	RW6_remove ELS & backfill for Bay 601 to Bay 606	8	8	07-Jan-22	15-Jan-22	31-Aug-21	09-Sep-21						
Z3_1218_1050	RW6_base slab construction for Bay 613 & Bay 614	16	16	30-Sep-21	20-Oct-21	30-Apr-21	20-May-21						
Z3_1218_1060	RW6_retaining wall construction for Bay 613 to 614	24	24	13-Nov-21	10-Dec-21	10-Jul-21	07-Aug-21						
RETAINING WALL NO.7													
Z3_1218_2000	RW7_ELS works for Bay 706 to Bay 711 (54m_2 side)	30	30	30-Nov-21	07-Jan-22	02-Jul-21	06-Aug-21						
Z3_1218_2010	RW7_base slab construction for Bay 706 to Bay 711	42	42	17-Dec-21	11-Feb-22	20-Jul-21	07-Sep-21						
Z3_1218_2050	RW7_base slab construction for Bay 701 & Bay 704	32	30	31-May-21 A	06-Nov-21	30-Apr-21	08-Jun-21						
Z3_1218_2060	RW7_retaining wall construction for Bay 701 to Bay 704	48	48	06-Nov-21	05-Jan-22	09-Jun-21	05-Aug-21						
MODIFY EXISTING RETAINING WALL SR3													
Z3_4920	SR3_ELS works for Bay SR301 to Bay SR306 (67m_1 side)	19	16	30-Aug-21 A	20-Oct-21	05-Nov-20	26-Nov-20						
Z3_4940	SR3_base slab construction for Bay SR301 to Bay SR306	42	39	07-Sep-21 A	04-Dec-21	24-May-21	14-Jul-21						
Z3_4950	SR3_retaining wall construction for Bay SR301 to SR306	60	60	26-Oct-21	07-Jan-22	22-Jun-21	01-Sep-21						
Z3_5050	SR3_retaining wall construction for Bay SR307 to SR311	50	30	17-May-21 A	12-Jan-22	14-Jul-21	10-Sep-21						
MODIFY EXISTING RETAINING WALL SR4													
Z3_5090	SR4_retaining wall construction for Bay SR401 to SR405	50	40	31-Oct-20 A	18-Nov-21	31-Oct-20	31-Dec-20						
Z3_5100	SR4_remove ELS & backfill for Bay SR401 to SR405	10	10	18-Nov-21	30-Nov-21	19-Jun-21	02-Jul-21						
Z3_5130	SR4_retaining wall construction for Bay SR406 to SR409	40	32	01-Feb-21 A	28-Dec-21	02-Jun-21	21-Jul-21						
Z3_5140	SR4_remove ELS & backfill for Bay SR406 to SR409	10	10	28-Dec-21	10-Jan-22	31-Jul-21	12-Aug-21						
MODIFY EXISTING SUBWAY NS30													
Z3_4542	Demolish existing subway & construct NS30	160	48	02-Dec-20 A	26-Nov-21	01-Feb-21	19-Aug-21						
WORK BETWEEN FOOTBRIDGE NF40 AND NF66 (ZONE 4)													
PRELIMINARIES WORKS													
SUMMARY PROGRAMME													
Z4SU1005	Zone 4 Stage 1 NB & SB foundation	434	238	06-Mar-20 A	21-Jul-22	31-Mar-20	16-Sep-21						
Z4SU1100	Zone 4 NF66 Construction	220	120	20-Jul-20 A	25-Feb-22	31-Aug-20	31-May-21						
Z4SU1110	Zone 4 NF40 Construction	387	163	12-Oct-19 A	21-Apr-22	06-Jan-20	28-Apr-21						
UTILITIES DIVERSION													
NORTHBOUND													
Z4_1280	UU_CATV-slew cable for N4 CH2190-2400 210m	25	25	17-Dec-21	18-Jan-22	11-Aug-21	08-Sep-21						
Z4_1300	UU_HKT-slew cable for N4 & NF66 CH2320-2360 40m	5	5	30-Sep-21	06-Oct-21	30-Apr-21	06-May-21						
SOUTHBOUND													
Z4_1380	UU_Salt watermain for S66 CH2275-2345 56m 700mm	20	20	14-Dec-21	10-Jan-22	06-Nov-21	30-Nov-21						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE FOUNDATION WORKS													
NORTHBOUND													
Z4_1520	N4_mini piles for N4-12 to N4-27 (126nr ver)	128	128	07-Oct-21*	12-Mar-22	31-May-21	01-Nov-21						
SOUTHBOUND													
Z4_1540	SE6_mini piles for S6E1-58 to S6E1-69 (70nr ver)	140	20	05-Jun-20 A	26-Oct-21	28-Sep-20	19-Mar-21						
PILE CAP AND FOOTING													
SOUTHBOUND													

- Remaining Level of Effort
- Remaining Work
- ◆ Milestone
- Actual Level of Effort
- Critical Remaining Work
- ◆ Baseline Milestone
- Actual Work
- Primary Baseline

ROAD WIDENING & RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)
3 Months Rolling Programme (30/9/21)
Page 5 of 7

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP11 Start	AP11 Finish	2021				2022		
								Sep 30	Oct 40	Nov 41	Dec 42	Jan 43		
Z4_1122	SE6_ELS for footing/cap construction S6E1-51P to S6E1-57 (86m_2 side)	48	16	12-Mar-21 A	21-Oct-21	09-Jun-21	06-Aug-21							
Z4_1126	SE6_footing/cap construction S6E1-51P to S6E1-57 (6nr)	42	21	13-May-21 A	15-Nov-21	21-Jun-21	10-Aug-21							
Z4_1130	SE6_ELS for cap construction S6E1-58 to S6E1-69 (145m_2 side)	40	30	26-Apr-21 A	25-Nov-21	21-Jun-21	07-Aug-21							
Z4_1140	SE6_footing/cap construction S6E1-58 to S6E1-69 (12nr)	84	77	18-Jun-21 A	19-Feb-22	10-Aug-21	19-Nov-21							
BRIDGE AND STRUCTURE WORKS														
MODIFICATION WORKS FOR NF40														
NF40_1090	Construct temporary support tower & jack up NF40	60	60	30-Sep-21	11-Dec-21	31-May-21	11-Aug-21							
NF40_1100	Demolish part of existing pier	30	30	11-Dec-21	19-Jan-22	11-Aug-21	15-Sep-21							
MODIFICATION WORKS FOR NF66														
NF66_1030	Erection temporary support tower	60	60	30-Sep-21	10-Dec-21	26-May-21	05-Aug-21							
NF66_1040	Remove existing column	60	60	11-Dec-21	25-Feb-22	06-Aug-21	18-Oct-21							
WORK BETWEEN FOOTBRIDGE NF66 AND FO TAN ROAD (ZONE 5)														
PRELIMINARIES WORKS														
SUMMARY PROGRAMME														
Z5SU1005	Zone 5 Stage 1 NB & SB foundation	467	267	10-Feb-20 A	24-Aug-22	31-Mar-20	28-Oct-21							
PREPARATORY WORKS														
MODIFICATION EXISTING ROAD/TEMPORARY ROAD														
Z5_1730	Zone 5-1_remove existing central barrier	21	21	30-Sep-21	01-Nov-21	02-Jul-21	02-Aug-21							
UTILITIES DIVERSION														
NORTHBOUND														
Z5_1630	UU_HGC-slew cable for N4 CH2575-2650 75m	9	5	01-Feb-21 A	06-Oct-21	08-May-21	18-May-21							
Z5_1640	UU_NWT-slew cable for N4 CH2580-2650 70m	15	15	06-Oct-21	25-Oct-21	20-May-21	05-Jun-21							
NOISE BARRIER AND SEMI-ENCLOSURE														
PILE FOUNDATION WORKS														
SOUTHBOUND														
Z5_1180	SE3-1_mini piles for S3E1-51 to S3E1-72 (132nr ver)	132	88	24-Jul-21 A	19-Feb-22	02-Aug-21	10-Jan-22							
SOUTHBOUND SLIP ROAD														
Z5_1300	R4_mini piles for R4-10P (12nr raking, 11nr ver)	92	50	29-Jul-21 A	29-Nov-21	03-Jun-21	20-Sep-21							
PILE CAP AND FOOTING														
NORTHBOUND														
Z5_1020	N4_ELS for footing/cap construction N4-29 to N4-53 (322m_2 side)	89	78	01-Feb-21 A	27-Jan-22	11-May-21	25-Aug-21							
Z5_1030	N4_cap/footing construction N4-29 to N4-53 (25nr)	147	132	27-Mar-21 A	22-Jun-22	25-May-21	17-Nov-21							
Z5_1050	N4_backfill & remove ELS	54	53	14-Apr-21 A	24-Aug-22	12-Feb-22	20-Apr-22							
SOUTHBOUND														
Z5_1190	SE3-1_ELS for footing/cap construction S3E1-51 to S3E1-72 (313m_2 side)	58	58	14-Dec-21	26-Feb-22	06-Nov-21	17-Jan-22							
Z5_1230	SE3-2_ELS for footing construction S3E2-51 to S3E2-61P (131m_2 side)	73	57	20-Mar-21 A	07-Dec-21	31-Mar-21	02-Jul-21							
Z5_1245	SE3-2_footing/cap construction S3E2-51 to 61P (9nr)	189	168	13-May-21 A	28-Apr-22	24-May-21	07-Jan-22							
SOUTHBOUND SLIP ROAD														
Z5_1260	N3_ELS for footing construction N3-01 to N3-02 (30m_2 side)	17	9	01-Oct-20 A	11-Oct-21	26-Feb-21	17-Mar-21							
Z5_1270	N3_footing construction N3-01 to N3-02 (2nr)	42	21	24-Oct-20 A	05-Nov-21	08-Apr-21	31-May-21							
Z5_1280	N3_backfill & remove ELS	5	3	23-Jan-21 A	08-Nov-21	07-Apr-21	14-Apr-21							
Z5_1310	R4_ELS for footing/cap construction R4-01 to R4-12P (158m_1 side)	44	29	08-Sep-20 A	13-Dec-21	18-Mar-21	13-May-21							
Z5_1320	R4_cap/footing construction R4-01 to R4-12P (8nr)	168	118	08-Oct-20 A	12-May-22	21-May-21	09-Dec-21							

- Remaining Level of Effort
- Remaining Work
- ◆ Milestone
- ◆ Baseline Milestone
- Actual Level of Effort
- Critical Remaining Work
- ◆ Baseline Milestone
- Actual Work
- Primary Baseline

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP11 Start	AP11 Finish	2021					2022
								Sep 39	Oct 40	Nov 41	Dec 42	Jan 43	
ROADWORKS AND REMAINING WORKS													
GEOTECHNICAL WORKS													
SOUTHBOUND SLIP ROAD													
Z5_1740	Zone 5 fill replacement by no-fines concrete 7SE-A/F166 (open excavation)	29	21	12-Mar-21 A	12-Aug-22	07-Apr-22	14-May-22						
PORTION E (ZONE 5)													
PRELIMINARIES WORKS													
SUMMARY PROGRAMME													
TPR NORTHBOUND													
PESU1000	Construction Zone 5 Portion E_Northbound structure	336	170	11-May-20 A	29-Apr-22	31-Jul-20	16-Sep-21						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE FOUNDATION WORKS													
NORTHBOUND SLIP ROAD													
Z5E_1200	N4 & R5_mini piles for N4-54P to R5-02P (16nr raking, 16nr ver)	64	38	09-Jul-21 A	16-Nov-21	24-May-21	07-Aug-21						
PILE CAP AND FOOTING													
NORTHBOUND SLIP ROAD													
Z5E_1020	R5_ELS for footing construction R5-02 to R5-07 (120m_1 side)	30	3	15-Apr-21 A	13-Oct-21	10-May-21	16-Jun-21						
Z5E_1030	R5_footing construction R5-03 to R5-07 (5nr)	63	35	04-Aug-21 A	24-Nov-21	16-Jun-21	30-Aug-21						
Z5E_1040	R5_backfill & remove ELS	30	30	24-Nov-21	31-Dec-21	30-Aug-21	06-Oct-21						
Z5E_1080	R6_backfill & remove ELS	13	13	24-Nov-21	09-Dec-21	29-Sep-21	16-Oct-21						
Z5E_1210	N4 & R5_ELS for pile cap construction N4-54P to R5-02P (15m_1 side)	5	5	16-Nov-21	22-Nov-21	09-Aug-21	13-Aug-21						
Z5E_1220	N4 & R5_cap/footing construction N4-52 to R5-02P (6nr)	63	63	22-Nov-21	10-Feb-22	14-Aug-21	29-Oct-21						
ROADWORKS AND REMAINING WORKS													
GEOTECHNICAL WORKS													
NORTHBOUND SLIP ROAD													
Z5E_1150	Zone 5 Portion E fill replacement by no-fines concrete 7SE-A/F163 (open excavation)	50	24	10-Sep-20 A	09-Mar-22	09-Dec-20	09-Feb-21						
Z5E_1160	Zone 5 Portion E fill replacement by no-fines concrete 7SE-A/FR136 (open excavation)	50	20	03-Jun-21 A	03-Nov-21	10-May-21	10-Jul-21						
Z5E_1170	Zone 5 Portion E fill replacement by no-fines concrete 7SE-A/F133 (open excavation)	38	8	10-Feb-20 A	09-Oct-21	11-Sep-20	28-Oct-20						

-  Remaining Level of Effort
-  Remaining Work
-  Milestone
-  Actual Level of Effort
-  Critical Remaining Work
-  Baseline Milestone
-  Actual Work
-  Primary Baseline

Date	Revision	Checked	Approved
11-Oct-21	3MRP DWP 2109	Tim	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com




Appendix B

Project Organization Chart

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com

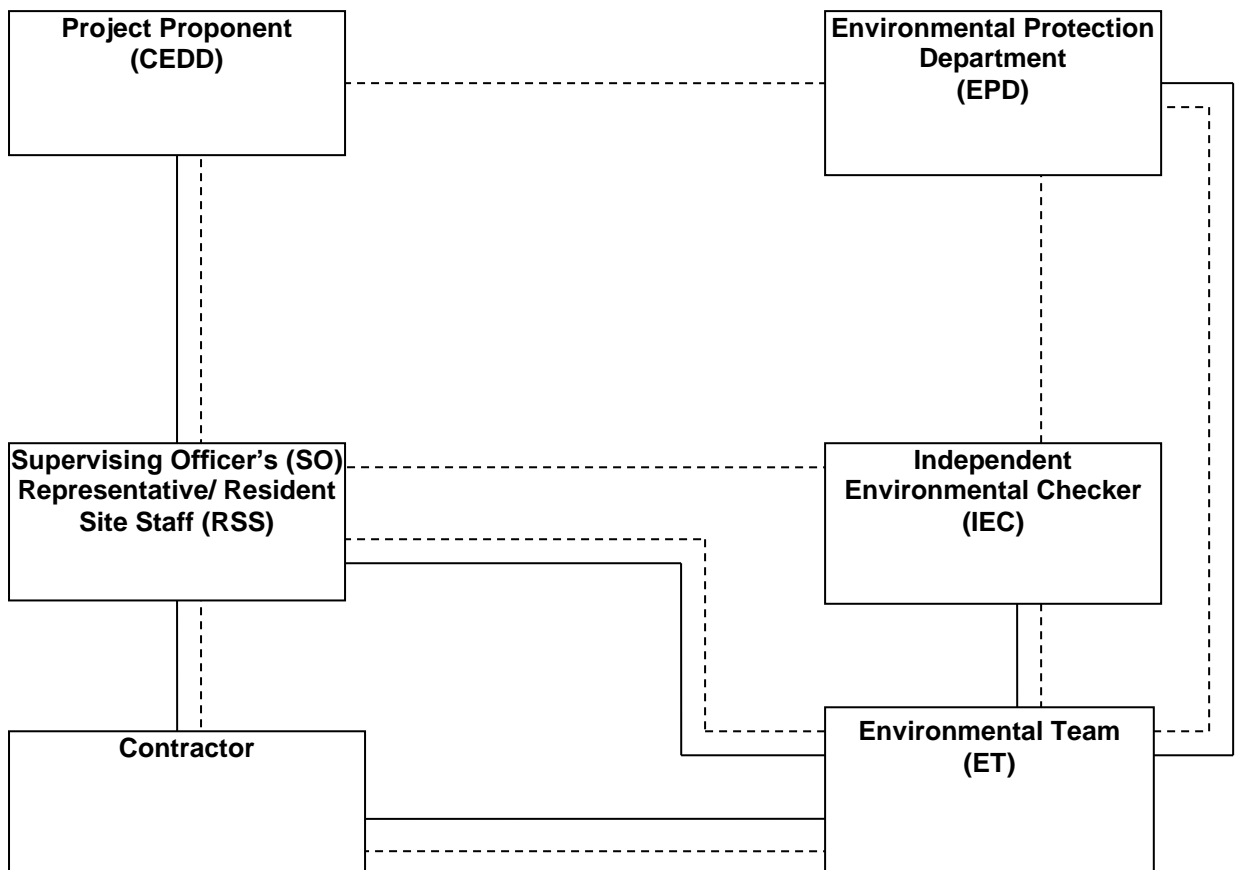

Legend:

- Line of Reporting
- - - Line of Communication

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix C

Action and Limit Levels for Air Quality and Noise

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Action and Limit Levels for 24-hr TSP and 1-hr TSP

Parameter	Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
24-hr TSP ($\mu\text{g}/\text{m}^3$)	AMS 5	156	260
	AMS 7A	171	
	AMS 14	174	
	AMS 15	172	
1-hr TSP ($\mu\text{g}/\text{m}^3$)	AMS 5	340	500
	AMS 7A	344	
	AMS 14	350	
	AMS 15	350	

Action and Limit Levels for Construction Noise, Leq (30min), dB(A)

Time Period	Location	Action	Limit
0700-1900 hrs on normal weekdays	NMS1	When one documented complaint is received	75 dB(A)
	NMS2		
	NMS3		
	NMS4		
	NMS5A		
	NMS6A		
	NMS7		
	NMS8		
	NMS9		
	NMS10A*		
	NMS11		
	NMS12*		
	NMS13		
	NMS14		
	NMS15		
	NMS16		
	NMS17*		
	NMS18		
	NMS19		
	NMS20		
NMS23			
NMS24			
NMS25A			
NMS26			
NMS27*			

* For NMS 10A, 12, 17 and 27, the Limit Level is reduced to 70 dB(A) for schools and 65 dB(A) during school examination periods.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix D

Calibration Certificates of Monitoring Equipment

Report no. : 940891CA202730

Page 1 of 1

CALIBRATION CERTIFICATE OF DUST METER

Client : Fugro Technical Services Limited

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Laser dust monitor
 Manufacturer : SIBATA
 Model No. : LD-3B
 Serial No. : 597305
 Specification Limit : NA
 Next Calibration Date : 22-Nov-2021

Laboratory Information

Description : 1. Balance 2. TSP high volume air sampler
 Equipment ID. / Serial no. : 1. C-065-9 2. 4350
 Date of Calibration : 23-Nov-2020 Ambient Temperature : 25 ± 10 °C
 Calibration Location : General Chemical Laboratory of FTS and Ma Wan A1 Site Boundary
 Method Used : By direct comparison the weight of dust particle trapped in a filter paper using high volume sampler (TSP method) for a certain period, with the reading of the UUT. They should be placed at the same location and powered on and off at the same time.

Calibration Results :

Reference concentration (mg/m ³)	Total count for 1 hour	CPM (Count per minute)
0.0915	3522	58.70
0.0469	2870	47.83
0.1172	3733	62.22

Remarks:

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The interpolation equation : Concentration (mg/m³) = K x [UUT reading (CPM)], where K = 0.001515
3. Correlation coefficient (r) : 0.9912

Checked by : C. Wong Date : 15-12-2020 Certified by : K.T. Leung Date : 15-12-2020
 CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)


**** End of Report ****

Correlation between HVS & Dust Meter

Model: Sibata LD-3B

Serial No: 597305

HVS - 24hr TSP $\mu\text{g}/\text{m}^3$	16.10	21.21	44.06	111.80	151.20	209.00
Dust Meter - 24hr CPM	9	14	29.1	74	99.7	138

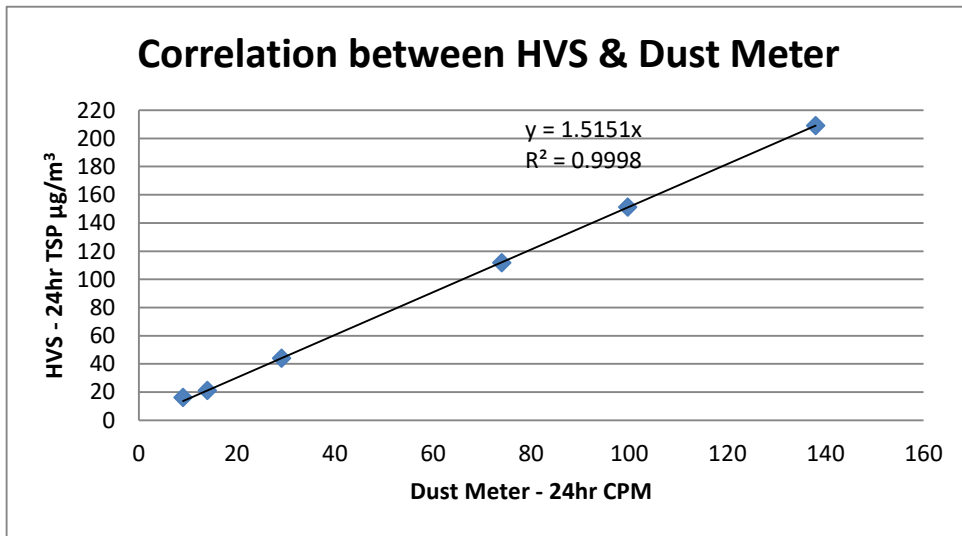

K factor = 1.515

Report no. : 940891CA202730(4)

Page 1 of 1

CALIBRATION CERTIFICATE OF DUST METER

Client : Fugro Technical Services Limited

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Laser dust monitor
Manufacturer : SIBATA
Model No. : LD-5R
Serial No. : 620407
Specification Limit : NA
Next Calibration Date : 22-Nov-2021

Laboratory Information

Description : 1. Balance 2. TSP high volume air sampler
Equipment ID. / Serial no. : 1. C-065-9 2. 4350
Date of Calibration : 23-Nov-2020 Ambient Temperature : 25 ± 10 °C
Calibration Location : General Chemical Laboratory of FTS and Ma Wan A1 Site Boundary
Method Used : By direct comparison the weight of dust particle trapped in a filter paper using high volume sampler (TSP method) for a certain period, with the reading of the UUT. They should be placed at the same location and powered on and off at the same time.

Calibration Results :

Reference concentration (mg/m ³)	Total count for 1 hour	CPM (Count per minute)
0.0915	3317	55.28
0.0469	3094	51.57
0.1172	3491	58.18

Remarks:

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The interpolation equation : Concentration (mg/m³) = K x [UUT reading (CPM)], where K = 0.001549
3. Correlation coefficient (r) : 0.9966

Checked by : Conny Date : 15-12-2020 Certified by : P.T. Leung Date : 15-12-2020

CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)


** End of Report **

Correlation between HVS & Dust Meter

Model: Sibata LD-5R

Serial No: 620407

HVS - 24hr TSP $\mu\text{g}/\text{m}^3$	15.59	22.19	45.99	115.23	161.56	213.96
Dust Meter - 24hr CPM	10.2	15.8	29	74.8	103.5	138.5

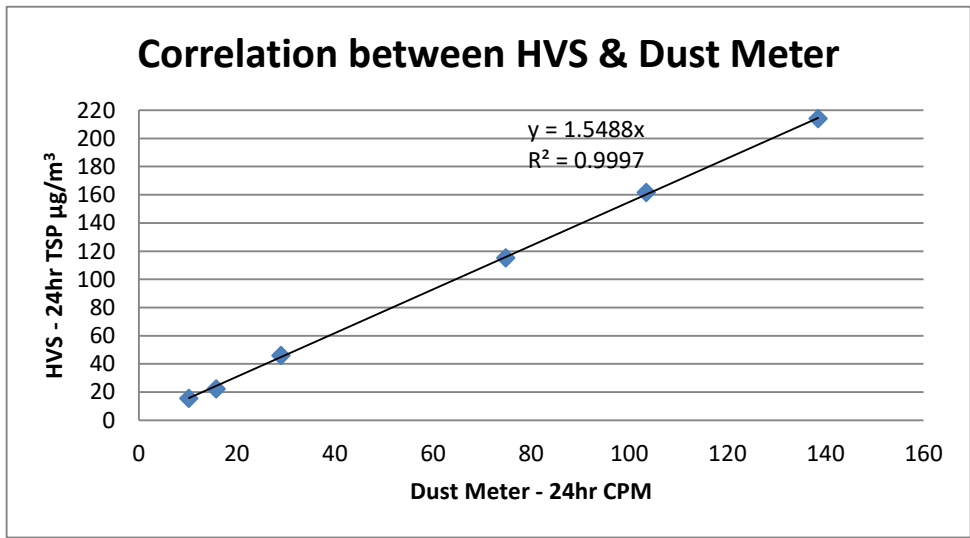

K factor = 1.549

Report no. : 940891CA202730(3)

Page 1 of 1

CALIBRATION CERTIFICATE OF DUST METER

Client : Fugro Technical Services Limited

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Laser dust monitor
 Manufacturer : SIBATA
 Model No. : LD-5R
 Serial No. : 620480
 Specification Limit : NA
 Next Calibration Date : 22-Nov-2021

Laboratory Information

Description : 1. Balance 2. TSP high volume air sampler
 Equipment ID. / Serial no. : 1. C-065-9 2. 4350
 Date of Calibration : 23-Nov-2020 Ambient Temperature : 25 ± 10 °C
 Calibration Location : General Chemical Laboratory of FTS and Ma Wan A1 Site Boundary
 Method Used : By direct comparison the weight of dust particle trapped in a filter paper using high volume sampler (TSP method) for a certain period, with the reading of the UUT. They should be placed at the same location and powered on and off at the same time.

Calibration Results :

Reference concentration (mg/m ³)	Total count for 1 hour	CPM (Count per minute)
0.0915	3211	53.52
0.0469	2732	45.53
0.1172	3659	60.98

Remarks:

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The interpolation equation : Concentration (mg/m³) = K x [UUT reading (CPM)], where K = 0.001597
3. Correlation coefficient (r) : 0.9909

Checked by : Canny Date : 15-12-2020 Certified by : K. Kwok Tai Date : 15-12-2020
 CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)


** End of Report **

Correlation between HVS & Dust Meter

Model: Sibata LD-5R

Serial No: 620480

HVS - 24hr TSP $\mu\text{g}/\text{m}^3$	16.87	25.87	50.57	119.72	163.92	218.16
Dust Meter - 24hr CPM	10.3	15.7	30	73.5	103	137.5

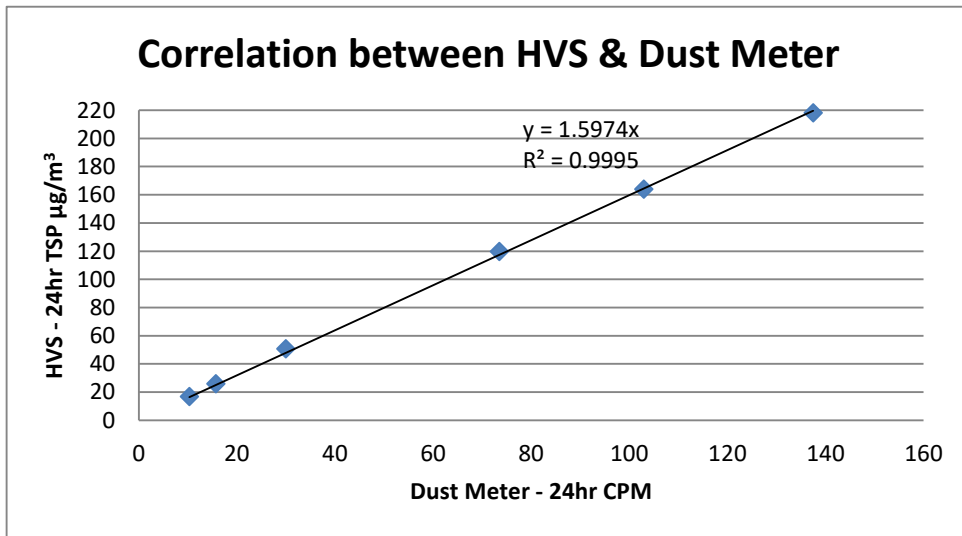

K factor = 1.597

Report no. : 940891CA202730(2)

Page 1 of 1

CALIBRATION CERTIFICATE OF DUST METER

Client : Fugro Technical Services Limited

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Laser dust monitor
 Manufacturer : SIBATA
 Model No. : LD-5R
 Serial No. : 882147
 Specification Limit : NA
 Next Calibration Date : 22-Nov-2021

Laboratory Information

Description : 1. Balance 2. TSP high volume air sampler
 Equipment ID. / Serial no. : 1. C-065-9 2. 4350
 Date of Calibration : 23-Nov-2020 Ambient Temperature : 25 ± 10 °C
 Calibration Location : General Chemical Laboratory of FTS and Ma Wan A1 Site Boundary
 Method Used : By direct comparison the weight of dust particle trapped in a filter paper using high volume sampler (TSP method) for a certain period, with the reading of the UUT. They should be placed at the same location and powered on and off at the same time.

Calibration Results :

Reference concentration (mg/m ³)	Total count for 1 hour	CPM (Count per minute)
0.0915	3424	57.07
0.0469	2818	46.97
0.1172	3629	60.48

Remarks:

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The interpolation equation : Concentration (mg/m³) = K x [UUT reading (CPM)], where K = 0.001554
3. Correlation coefficient (r) : 0.9923

Checked by : Cherry Date : 15-12-2020 Certified by : K.T. Young Date : 15-12-2020

CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)


** End of Report **

Correlation between HVS & Dust Meter

Model: Sibata LD-5R

Serial No: 882147

HVS - 24hr TSP $\mu\text{g}/\text{m}^3$	25.015	35.463	47.554	130.95	198.76
Dust Meter - 24hr CPM	18.5	24.5	30.4	84.5	125.6

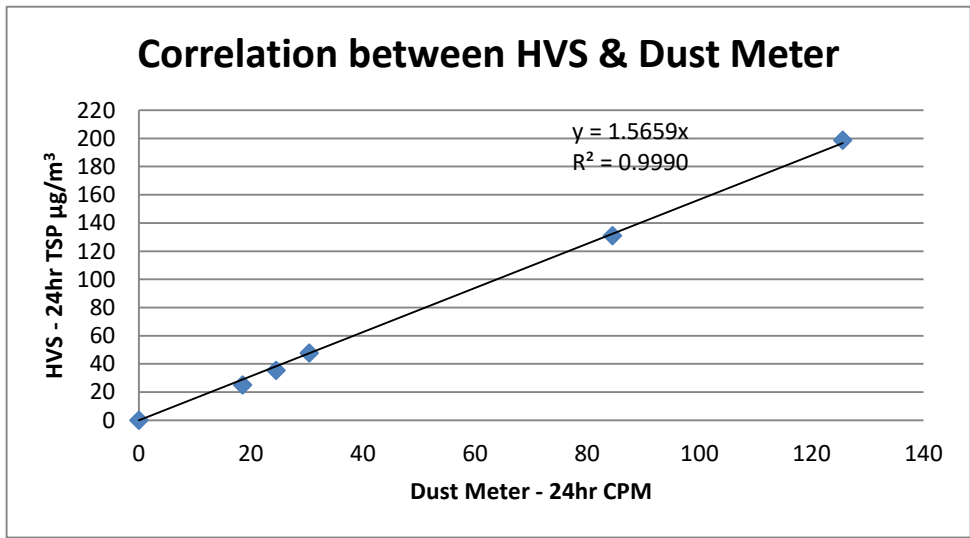

K factor = 1.554

Report no.: 203258CA202751

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT

 Description : Sound Level Meter
 Manufacturer : Casella

	Meter	Microphone	Preamplifier
Model No.	CEL-63X	CE-251	CEL-495
Serial No.	1488271	01910	004065

Equipment ID : N-52

Next Calibration Date : 21-Dec-2021

Specification Limit : EN 61672-1: 2003 Class 1

Laboratory Information

Details of Reference Equipment -

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)

Equipment ID. : R-108-1

Date of Calibration : 22-Dec-2020

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters		Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	2.1	2.6 to -0.6
	2000Hz	1.4	2.8 to -0.4
	1000Hz	0.0	1.1 to -1.1
	500Hz	-3.5	-1.8 to -4.6
	250Hz	-8.8	-7.2 to -10.0
	125Hz	-16.3	-14.6 to -17.6
	63Hz	-26.3	-24.7 to -27.7
	31.5Hz	-39.2	-37.4 to -41.4
Differential level linearity	94dB-104dB	0.0	± 0.6
	104dB-114dB	0.0	± 0.6

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast.
4. The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
5. The values given in this Calibration Certificate only relate to the values at the time of the test and any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

 Checked by : William Date : 28-12-2020 Certified by : F. Leung Date : 28-12-2020
 CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

** End of Report **

Report no.: 203258CA210154

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT

Description : Sound Level Meter

Manufacturer : Casella

	Meter	Microphone	Preamplifier
Model No.	CEL-63X	CE-251	CEL-495
Serial No.	1488287	02552	002110

Equipment ID : N/A

Next Calibration Date : 20-Jan-2022

Specification Limit : EN 61672-1: 2003 Class 1

Laboratory Information

Details of Reference Equipment -

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)

Equipment ID. : R-108-1

Date of Calibration : 21-Jan-2021

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters		Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	-0.6	2.6 to -0.6
	2000Hz	1.1	2.8 to -0.4
	1000Hz	0.9	1.1 to -1.1
	500Hz	-2.0	-1.8 to -4.6
	250Hz	-7.3	-7.2 to -10.0
	125Hz	-14.7	-14.6 to -17.6
	63Hz	-24.8	-24.7 to -27.7
	31.5Hz	-37.9	-37.4 to -41.4
Differential level linearity	94dB-104dB	0.0	± 0.6
	104dB-114dB	0.0	± 0.6

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast.
4. The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
5. The values given in this Calibration Certificate only relate to the values at the time of the test and any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

 Checked by : William Date : 22-1-2021 Certified by : Leung Kwok Tai Date : 22-1-2021
 CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

**** End of Report ****

Report no.: 212769CA211755

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Address : Room 723 & 725, 7/F., Block B Profit Industrial Building, 1-15 Kwai Fung Crescent, Kwai Chung, N.T.

Project : Calibration Services

Details of Unit Under Test, UUT

Description	: Sound Level Meter									
Manufacturer	: Casella									
Model No.	: <table border="1" style="display: inline-table; border-collapse: collapse;"> <tr> <td>Meter</td> <td>Microphone</td> <td>Preamplifier</td> </tr> <tr> <td>CEL-63X</td> <td>CE-251</td> <td>CEL-495</td> </tr> <tr> <td>1488293</td> <td>04064</td> <td>004061</td> </tr> </table>	Meter	Microphone	Preamplifier	CEL-63X	CE-251	CEL-495	1488293	04064	004061
Meter	Microphone	Preamplifier								
CEL-63X	CE-251	CEL-495								
1488293	04064	004061								
Serial No.	: <table border="1" style="display: inline-table; border-collapse: collapse;"> <tr> <td>Meter</td> <td>Microphone</td> <td>Preamplifier</td> </tr> <tr> <td>CEL-63X</td> <td>CE-251</td> <td>CEL-495</td> </tr> <tr> <td>1488293</td> <td>04064</td> <td>004061</td> </tr> </table>	Meter	Microphone	Preamplifier	CEL-63X	CE-251	CEL-495	1488293	04064	004061
Meter	Microphone	Preamplifier								
CEL-63X	CE-251	CEL-495								
1488293	04064	004061								
Equipment ID	: N/A									
Next Calibration Date	: 25-Jul-2022									
Specification Limit	: EN 61672-1: 2003 Class 1									

Laboratory Information

Details of Reference Equipment -

Description	: B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)
Equipment ID.	: R-108-1

Date of Calibration : 26-Jul-2021

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters	Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	1.0 2.6 to -0.6
	2000Hz	1.2 2.8 to -0.4
	1000Hz	0.0 1.1 to -1.1
	500Hz	-3.4 -1.8 to -4.6
	250Hz	-8.7 -7.2 to -10.0
	125Hz	-16.2 -14.6 to -17.6
	63Hz	-26.1 -24.7 to -27.7
	31.5Hz	-38.9 -37.4 to -41.4
Differential level linearity	94dB-104dB	± 0.6
	104dB-114dB	± 0.6

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The expanded uncertainty is 0.3 dB with a coverage factor of 2 at a confidence level of 95%.
4. For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast
5. The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
6. The values given in this Calibration Certificate only relate to unit under test and the values measured at the time of the test. Any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

 Checked by : Cenny Date : 30-7-2021 Certified by : K.T. Leung Date : 30-7-2021
 CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

**** End of Report ****

Report no.: 203258CA202302(2)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT

 Description : Sound Level Meter
 Manufacturer : Casella

	Meter	Microphone	Preamplifier
Model No.	CEL-63X	CE-251	CEL-495
Serial No.	1488304	03876	002752

Equipment ID : N-62

Next Calibration Date : 29-Oct-2021

Specification Limit : EN 61672-1: 2003 Class 1

Laboratory Information

Details of Reference Equipment -

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)

Equipment ID. : R-108-1

Date of Calibration : 30-Oct-2020

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters	Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	1.5 2.6 to -0.6
	2000Hz	1.3 2.8 to -0.4
	1000Hz	-0.1 1.1 to -1.1
	500Hz	-3.5 -1.8 to -4.6
	250Hz	-8.9 -7.2 to -10.0
	125Hz	-16.4 -14.6 to -17.6
	63Hz	-26.4 -24.7 to -27.7
	31.5Hz	-39.4 -37.4 to -41.4
Differential level linearity	94dB-104dB	0.0 ± 0.6
	104dB-114dB	0.0 ± 0.6

Remarks :

- The equipment used in this calibration is traceable to recognized National Standards.
- The mean value is the average of four measurements.
- For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast.
- The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
- The values given in this Calibration Certificate only relate to the values at the time of the test and any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

 Checked by : K. Kwok Date : 4-11-2020 Certified by : K.T. Leung Date : 4-11-2020
 CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

** End of Report **

Report no.: 212769CA212069(3)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
Manufacturer : Casella (Model CEL-120/1)
Serial No. : 2383707
Equipment ID : N/A

Next Calibration Date : 25-Aug-2022

Specification Limit : EN 60942: 2003 Class 1

Laboratory Information

Details of Calibration Equipment

Description : Reference Sound level meter
Equipment ID. : R-119-2

Date of Calibration : 26-Aug-2021

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	-0.4 dB	±0.4dB
114dB	-0.3 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The unit under test complies with the specification limit.
4. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties quoted will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

Checked by : Canny Date : 27-8-2021 Certified by : K. Leung Date : 27-8-2021
CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

**** End of Report ****

Report no.: 212769CA211663

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
 Manufacturer : Casella (Model CEL-120/1)
 Serial No. : 2383886
 Equipment ID : N/A
 Next Calibration Date : 15-Jul-2022
 Specification Limit : EN 60942: 2003 Class 1

Laboratory Information

Details of Calibration Equipment

Description : Reference Sound level meter
 Equipment ID. : R-119-2
 Date of Calibration : 16-Jul-2021
 Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C
 Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	0.3 dB	±0.4dB
114dB	0.4 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The expanded uncertainty is 0.3 dB with a coverage factor of 2 at a confidence level of 95%.
4. The unit under test complies with the specification limit.
5. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties quoted will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

Checked by : Cenny Date : 20-7-2021 Certified by : K.T. Leung Date : 20-7-2021
 CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

** End of Report **

Report no.: 203258CA210891

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
 Manufacturer : Casella (Model CEL-120/1)
 Serial No. : 4358251
 Equipment ID : N-34

Next Calibration Date : 10-May-2022

Specification Limit : EN 60942: 2003 Class 1

Laboratory Information

Details of Calibration Equipment

Description : Reference Sound level meter
 Equipment ID. : R-119-2

Date of Calibration : 11-May-2021

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	-0.1 dB	±0.4dB
114dB	-0.1 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The unit under test complies with the specification limit.
4. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

 Checked by : William Date : 12-5-2021 Certified by : R. T. Leung Date : 12-5-2021

CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

** End of Report **

Report no.: 212769CA212279(2)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Client Supplied Information

Details of Unit Under Test, UUT

Description : Sound Calibrator
 Manufacturer : Casella (Model CEL-120/1)
 Serial No. : 5230736
 Equipment ID : N/A

Next Calibration Date : 12-Sep-2022

Specification Limit : EN 60942: 2003 Class 1

Laboratory Information

Details of Calibration Equipment

Description : Reference Sound level meter
 Equipment ID. : R-119-2

Date of Calibration : 13-Sep-2021

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	-0.1 dB	±0.4dB
114dB	-0.1 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The unit under test complies with the specification limit.
4. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties quoted will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

 Checked by : Conny Date : 17-9-2021 Certified by : E.T. Leung Date : 17-9-2021

CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

**** End of Report ****

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix E

Environmental Monitoring Schedules, Examination Schedules and Arrangements on Deferral of Class Resumption for All Schools

Project: Contract No.: NE/2017/05 - Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
							1
							2
	3		4	5	6	7	8
			AMSS Tin Liu AMS7A Sheung Wo Che AMS14 Ha Wo Che AMS15 Ha Wo Che				
			NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26			
	10		11	12	13	14	15
		AMSS Tin Liu AMS7A Sheung Wo Che AMS14 Ha Wo Che AMS15 Ha Wo Che					AMSS Tin Liu AMS7A Sheung Wo Che AMS14 Ha Wo Che AMS15 Ha Wo Che
		NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26				
	17		18	19	20	21	22
						AMSS Tin Liu AMS7A Sheung Wo Che AMS14 Ha Wo Che AMS15 Ha Wo Che	
						NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26
	24		25	26	27	28	29
					AMSS Tin Liu AMS7A Sheung Wo Che AMS14 Ha Wo Che AMS15 Ha Wo Che		
					NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26	
	31						

- Remark
- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 - The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.
 - According to the Hong Kong Observatory, anticipated wind directions in October 2021 are north, north east and east.
 - According to the Contractor, the anticipated major construction activities in the reporting month includes:
 - Tree Preservation, Felling, Pruning, Transplantation in Zone 1, 2, 3, 4 and 5.
 - Road Surface Maintenance in Zone 1, 2, 3, 4 and 5.
 - Noise Barrier Foundation Works in Zone 1, 2, 4 and 5.
 - Noise Barrier Erection Works in Zone 1 and 2.
 - Road Reconstruction Works, Sheet Pile Removal and Lane Shifting Works in Zone 1 and 2.
 - Trial Pits Excavation in Zone 3, 4 and 5.
 - Construction, Diversion of Underground Utilities, including ELS works and Sheet Piling in Zone 3 and 5.
 - Retaining Wall Construction Works in Zone 3.
 - Construction of Cycle Track Subway, Pump Room and Stem Wall Construction Works in Zone 3.
 - Demolition of Existing Parapet and Lagging Wall Construction Works in Zone 3.
 - Construction work for Temporary Site Access Relocation in Zone 3.
 - Pre Bore H Pile Construction Works and Steel Works Installation for Lift in Zone 3.
 - Profile Barrier, Stem Wall Construction Works and Foundation Works for SR2 in Zone 3.
 - Construction Works for N263 Bridge Deck Widening and SR6 Temporary Widening in Zone 3.
 - ELS Works at SHA for Widening of SR3 in Zone 3.
 - Piezometer for underground water pressure measurement in Zone 3.
 - NF40 and N66 Footbridge Construction Works in Zone 4.
 - Mini Pile Construction Works in Zone 4 and 5.
 - Erection of 7m Height Fencing in Zone 4.
 - Stem Wall and Drainage Construction Works in Zone 5.

Project: Contract No.: NE/2017/05 - Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday	
Nov-21			1	2	3	4	5	6
					AMS 4A Wai Wah Centre AMS 7A Sheung Wo Che AMS 12 Fung Wo Estate AMS 17 Wo Che Estate			
					NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26		
	7		8	9	10	11	12	13
				AMS 4A Wai Wah Centre AMS 7A Sheung Wo Che AMS 12 Fung Wo Estate AMS 17 Wo Che Estate				
				NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26			
	14		15	16	17	18	19	20
		AMS 4A Wai Wah Centre AMS 7A Sheung Wo Che AMS 12 Fung Wo Estate AMS 17 Wo Che Estate						AMS 4A Wai Wah Centre AMS 7A Sheung Wo Che AMS 12 Fung Wo Estate AMS 17 Wo Che Estate
		NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26					
	21		22	23	24	25	26	27
							AMS 4A Wai Wah Centre AMS 7A Sheung Wo Che AMS 12 Fung Wo Estate AMS 17 Wo Che Estate	
							NMS 1, NMS 2, NMS 3, NMS 4, NMS 5A, NMS 6A, NMS 7, NMS 15, NMS 16, NMS 18,NMS 23, NMS 27	NMS 8, NMS9, NMS 10A, NMS 11, NMS 12, NMS 13, NMS 14, NMS17, NMS 19, NMS 20, NMS 24, NMS 25A, NMS 26
	28		29	30				

- Remark
- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 - The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.
 - According to the Hong Kong Observatory, anticipated wind directions in November 2021 are north, northeast and east.
 - According to the Contractor, the anticipated major construction activities in the reporting month includes:
 - Tree Preservation, Felling, Pruning, Transplantation in Zone 1, 2 and 3.
 - Road Surface Maintenance in Zone 1, 2, 3, 4 and 5.
 - Noise Barrier Foundation Works in Zone 1, 2, 4 and 5.
 - Noise Barrier Erection Works in Zone 1 and 2.
 - Road Reconstruction Works, Sheet Pile Removal and Lane Shifting Works in Zone 1 and 2.
 - Trial Pits Excavation in Zone 3.
 - Construction, Diversion of Underground Utilities, including ELS works and Sheet Piling in Zone 3.
 - Retaining Wall Construction Works in Zone 3.
 - Construction of Cycle Track Subway, Pump Room and Stem Wall Construction Works in Zone 3.
 - Demolition of Existing Parapet and Lagging Wall Construction Works in Zone 3.
 - Pre Bore H Pile Construction Works and Steel Works Installation for Lift in Zone 3.
 - Profile Barrier, Stem Wall Construction Works and Foundation Works for SR2 in Zone 3.
 - Construction Works for N263 & N264 Bridge Deck Widening and SR6 Temporary Widening in Zone 3.
 - ELS Works at SHA for Widening of SR3 in Zone 3.
 - Piezometer for Underground Water Pressure Measurement in Zone 3.
 - NF40 Footbridge Construction Works in Zone 4.
 - Erection of 7m Height Fencing and Protection Measure for MTRC Railway in Zone 4.
 - Mini Pile Construction Works in Zone 5.
 - Stem Wall and Drainage Construction Works in Zone 5.



Project: Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

Regular Night Time Noise Monitoring Schedule (October 2021)

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4	5	6	7 Regular night time noise monitoring	8	9
10	11 Regular night time noise monitoring	12	13	14	15	16
17	18	19	20	21 Regular night time noise monitoring	22	23
24	25	26	27	28 Regular night time noise monitoring	29	30
31						

Remarks

1. Due to safety concern, 2 staffs will carry out the night time noise monitoring together at all 21 monitoring stations on the same monitoring night of each week.
2. Actual monitoring schedule may be subjected to change due to any safety concern or adverse weather condition.

FUGRO TECHNICAL SERVICES LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong

Tel : (852)-24508238
Fax : (852)-24508032
Email : mcl@fugro.com



Project: Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

Tentative Regular Night Time Noise Monitoring Schedule (November 2021)

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4 Regular night time noise monitoring	5	6
7	8	9	10	11 Regular night time noise monitoring	12	13
14	15	16	17	18 Regular night time noise monitoring	19	20
21	22	23	24	25 Regular night time noise monitoring	26	27
28	29	30				

Remarks

1. Due to safety concern, 2 staffs will carry out the night time noise monitoring together at all 21 monitoring stations on the same monitoring night of each week.
2. Actual monitoring schedule may be subjected to change due to any safety concern or adverse weather condition.

沙田崇真學校

2021 - 22 年度校曆表

27/8/2021 更新

日 一 二 三 四 五 六							假期 / 事項							日 一 二 三 四 五 六							假期 / 事項						
九 月				1	2	3	4	上學期開始(1/9) P. 2-6 半天上課 (1-8/9) P. 1 半天上課 (1-10/9)	四 月							1	2	家長日(2/4) 清明節(5/4) 福音周及復活節崇拜 (7-8/4) 復活節假期(11/4-19/4)									
	5	6	7	8	9	10	11			3	4	5	6	7	8	9											
	12	13	14	15	16	17	18			10	11	12	13	14	15	16											
	19	20	21	22	23	24	25			17	18	19	20	21	22	23											
							中秋節翌日(22/9)										24	25	26	27	28	29	30	綵排日(28/4)校慶崇拜及晚會(29/4)			
十 月						2	國慶日(1/10)	五 月	1	2	3	4	5	6	7	勞動節(1/5)勞動節補假(2/5) 零功課日(5/5) 佛誕補假(9/5)											
	3	4	5	6	7	8	9		8	9	10	11	12	13	14												
	10	11	12	13	14	15	16		零功課日(11/10)重陽節 (14/10)	15	16	17	18	19	20		21										
	17	18	19	20	21	22	23			22	23	24	25	26	27		28										
	24	25	26	27	28	29	30			29	30	31															
	31																	預考周(23/5-30/5) 一至六年級考試(31/5-7/6)									
十一 月		1	2	3	4	5	6	預考周(8/11-16/11) 一至六年級考試(17/11-23/11)	六 月					1	2	3	4	端午節(3/6) 全港性系統評估 (8-9/6) 教師專業發展日(13/6) 畢業禮(30/6)									
	7	8	9	10	11	12	13			5	6	7	8	9	10	11											
	14	15	16	17	18	19	20			12	13	14	15	16	17	18											
	21	22	23	24	25	26	27			19	20	21	22	23	24	25											
								26	27	28	29	30															
十二 月			1	2	3	4	全方位活動日 (2/12) 學校假期(3/12)	七 月							2	香港特區成立紀念日 (1/7) 教師專業發展日(15/7) 暑假(16/7-31/8)											
	5	6	7	8	9	10	11		3	4	5	6	7	8	9												
	12	13	14	15	16	17	18		10	11	12	13	14	15	16												
	19	20	21	22	23	24	25		17	18	19	20	21	22	23												
	26	27	28	29	30	31			24	25	26	27	28	29	30												
							聖誕崇拜 (17/12) 立法會選舉翌日假期(20/12) 陸運會 (21/12) 聖誕及新年假期(22/12-2/1)		31																		
二零二二 年一月						1	六年級教育營(3-5/1) 一至五級專題研習周(3-6/1) 教師專業發展日(7/1) P. 6 家長日(8/1) P. 1-5 家長日(15/1) 零功課日(19/1) 跨學科活動日 (27/1)	八 月									綠 色 為 半 天 上 課 日 橙 色 為 延 伸 學 習 活 動 課 (周 三) 紅 色 為 公 眾 假 期 本年度上課日數：190 日 學校假期：88 日 學校自決假期：3 日 周六及日(不包長假期)：81 日 教師專業發展日：3 日 合計：365 日										
	2	3	4	5	6	7			8	7	8	9	10	11	12	13											
	9	10	11	12	13	14			15	14	15	16	17	18	19	20											
	16	17	18	19	20	21			22	21	22	23	24	25	26	27											
	23	24	25	26	27	28			29	28	29	30	31														
								30	31																		
二 月			1	2	3	4	5	農曆新年假期(28/1-8/2) 下學期開始(9/2) 預考周(14/2-22/2) 六年級報分試(23/2-1/3) 一至五年級主科考試(28/2-1/3)	學校假期	6	7	8	9	10	11	12	學校自決假期										
	13	14	15	16	17	18	19			13/6	15/7	教師專業發展日															
	20	21	22	23	24	25	26																				
									27	28																	
三 月			1	2	3	4	5	學校旅行(17/3) 學校假期(18/3) 學校籌款日 (27/3) 學校假期(28/3)	7/1	6	7	8	9	10	11	12											
	13	14	15	16	17	18	19																				
	20	21	22	23	24	25	26																				
	27	28	29	30	31																						

新界沙田瀝源邨

網址：www.stts.edu.hk

電話：3576 3344

傳真：2609 0597

校長姓名：洪細君女士

校長簽署：_____

日期：27-8-2021

聖公會主風小學 2021-2022 年度上學期校曆表

週次	月份	星 期							行 事 要 項	假期日數		
		日	一	二	三	四	五	六				
①	2021				1*	2	3	4	1/9 上學期開學日			
②	九 月	5	6	7	8	9	10	11				
③		12	13	14	15	16	17	18				
④		19	20	21*	22	23	24	25			21/9 教師專業發展日 22/9 中秋節翌日	1
⑤		26	27	28	29	30						
⑥	十 月						1	2	1/10 國慶日	1		
⑦		3	4	5	6	7	8	9	14/10 重陽節	1		
⑧		10	11	12	13	14	15	16				
⑨		17	18	19	20	21	22	23	26/10-29/10 進展性評估(J.2-J.5)/呈分試(J.6)			
⑩		24	25	<u>26</u>	<u>27</u>	<u>28</u>	<u>29</u>	30				
⑩	31											
⑪	十 一 月		1	2	3	4	5	6	12/11 第十四屆陸運會 20/11 上學期家長日、J.6 家長會			
⑫		7	8	9	10	11	12*	13				
⑬		14	15	16	17	18	19	20*				
⑭		21	22	23	24	25	26	27				
⑭	28	29	30									
⑮	十 二 月				1	2	3	4	9/12 教師專業發展日 13/12-16/12 上學期學期試 20/12 選舉日翌日 21/12/2021-1/1/2022 聖誕及新年假期	1 5 6		
⑯		5	6	7	8	9*	10	11				
⑰		12	<u>13</u>	<u>14</u>	<u>15</u>	<u>16</u>	17	18				
⑱		19	20	21	22	23	24	25				
⑲	26	27	28	29	30	31						
⑲	2022							1		1		
⑳	一 月	2	3	4	5	6	7	8	17/1 下學期開始 26/1-28/1 教育營(J.6) 27/1 旅行日(J.1-J.5) 31/1-10/2 農曆新年假期	1		
		9	10	11	12	13	14	15				
		16	17*	18	19	20	21	22				
		23	24	25	26*	27*	28*	29				
		30	31									
	二 月			1	2	3	4	5		5 5		
		6	7	8	9	10	11	12				
		13	14	15	16	17	18	19				

附註： □代表假期 *代表特別事宜

培英中學2021至2022年度校曆表

		日	一	二	三	四	五	六	假期及注意事項
週次	八	(15)	(16)	(17)	(18)	(19)	(20)	(21)	
		(22)	(23)	(24)	(25)	(26)	(27)	(28)	
1	九	(29)	(30)	(31)	Sept 1	2	3	4	(1/9)開學禮 (2/9)正式上課
		5	6	7	8	9	10	11	(10/9)開學崇拜會
2	十	12	13	14	15	16	17	18	(13/9)中一至中四學生開始繳交周記 (14/9)各班拍攝學生相片 (13-17/9)藝術周
		19	20	21	(22)	23	24	25	(22/9)中秋節翌日假期 (24/9)學生會候選內閣論壇
3	月	26	27	28	29	30	Oct (1)	2	(27-30/9)學生會網上選舉 (27-30/9)個人社會及人文領域周 (1/10)國慶日假期
		3	4	5	6	7	8	9	(9/10)香港培英校友會校友日
4	十	10	11	12	13	(14)	(15)	16	(14/10)重陽節假期 (15/10)教師專業發展日(1)
		17	18	19	20	21	22	23	
5	月	24	25 ^T	26 ^T	27 ^T	28 ^T	29 ^T	30	(25-29/10)中一至中六級統一測驗
		31	Nov 1 [△]	(2)	3	4	5	6	(1/11)第六十一屆陸運會 (2/11)陸運會翌日假期 (5/11)學生領袖就職典禮
6	一	7	8	9	10	11	12	13 [△]	(8-12/11)數學周 (13/11下午)家長教師會第二十四屆會員大會
		14	15	16	17	18	19	20	
7	月	21 [△]	22	23	24	25	26	27	(21/11)南區中學巡禮 (22-26/11)敬師周 (26/11)師生聯誼日
		28	29	30	Dec 1	2	3 [△]	4	(3/12)全方位學習日
8	二	5	6	7	8	9	10	11	(6-10/12)英語周 (7/12)拍攝畢業照及班相 (11/12)中西南區小學數學比賽
		12	13	14	15	16	17	18	(14-16/12)中六級校外模擬考試 (17/12)聖誕崇拜及慶祝會
9	月	19	(20)	(21)	(22)	(23)	(24)	(25)	(20/12)立法會選舉翌日假期 (21/12-1/1)聖誕及新年假期共12天
		(26)	(27)	(28)	(29)	(30)	(31)	(1)	Jan (21-24,28-30/12)中六級補課
10	一	2	3	4	5	6	7 ^E	8	(7-18/1)中一至中五級上學期期考共8天 (7-20/1)中六級畢業試
		9	10 ^E	11 ^E	12 ^E	13 ^E	14 ^E	15	
11	月	16	17 ^E	18 ^E	19 ^E	20 ^E	21	22	(19-21/1)中一至中五級試後回饋日 (21/1-10/3)中六級試後上課 (21/1下午)中五級學習概覽講座
		23	24	25	26	27	28	29	(24-26/1)中一至中五級溫習及補考
12	二	30	(31)	(1)	(2)	(3)	(4)	(5)	(31/1-12/2)農曆新年假期共13天
		(6)	(7)	(8)	(9)	(10)	(11)	(12)	
13	月	13	14	15	16	17	(18)	19	(14/2)下學期開始 (14-17/2)中華文化周 (18/2)區會中、小、幼聯校教師發展日
		20	21	22	23	24	25	26	(25/2)區會中、小、幼聯校教師發展日(後備) (21/2)中一至中四級學生開始繳交周記 (21-25/2)福音周 (25/2)佈道會

() - 假期 ^E - 考試 [△] - 特別活動 教師發展日，學生不用上課

週日	週一	週二	週三	週四	週五	週六
26	27	28	29	30	1	2
	Week 5			Student Bodies Joint	National Day	
3	4	5	6	7	8	9
	Week 6					下午2點 - PTA AGM
10	11	12	13	14	15	16
	Week 7			Chung Yeung		
17	18	19	20	21	22	23
	Week 8				F.4 Parents' Night	
24	25	26	27	28	29	30
	Week 9				F.1 & F.2 Parents'	
31	1	2	3	4	5	6
	Week 10			Athletics Meet		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix F

Air Quality Monitoring Data

1-hour TSP Impact Monitoring Result for NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

AMS5 - Tin Liu

1-hour TSP ($\mu\text{g}/\text{m}^3$)								
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather
05-Oct-21	13:05	58	58	53	56	340	500	Fine
11-Oct-21	15:00	67	67	47	60			Fine
16-Oct-21	18:16	41	56	58	52			Fine
22-Oct-21	17:40	67	73	68	69			Fine
28-Oct-21	11:20	64	55	58	59			Fine
Average		59						
Max		73						
Min		41						

AMS 7A - Sheung Wo Che

1-hour TSP ($\mu\text{g}/\text{m}^3$)								
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather
05-Oct-21	18:22	54	53	53	53	344	500	Fine
11-Oct-21	14:16	67	62	57	62			Fine
16-Oct-21	07:33	64	50	57	57			Fine
22-Oct-21	17:54	61	57	54	57			Fine
28-Oct-21	16:38	60	53	56	56			Fine
Average		57						
Max		67						
Min		50						

AMS 14 - Ha Wo Che


1-hour TSP ($\mu\text{g}/\text{m}^3$)								
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather
05-Oct-21	09:41	56	57	48	54	350	500	Fine
11-Oct-21	12:32	62	64	62	63			Fine
16-Oct-21	07:49	53	48	57	53			Fine
22-Oct-21	16:16	70	67	66	68			Fine
28-Oct-21	16:52	61	64	51	59			Fine
Average		59						
Max		70						
Min		48						

AMS 15 - Ha Wo Che


1-hour TSP ($\mu\text{g}/\text{m}^3$)								
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather
05-Oct-21	13:55	42	51	62	52	350	500	Fine
11-Oct-21	17:45	64	65	62	64			Fine
16-Oct-21	15:02	51	56	54	54			Fine
22-Oct-21	12:24	64	69	66	66			Fine
28-Oct-21	17:03	51	57	54	54			Fine
Average		58						
Max		69						
Min		42						

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.


1-hr TSP Monitoring record for AMS 5

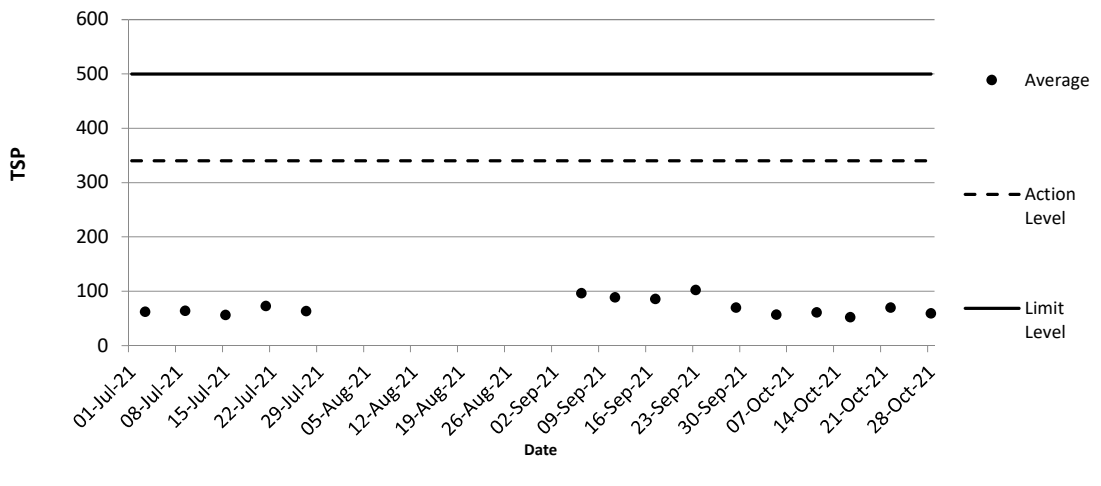


1-hr TSP Monitoring record for AMS 7A

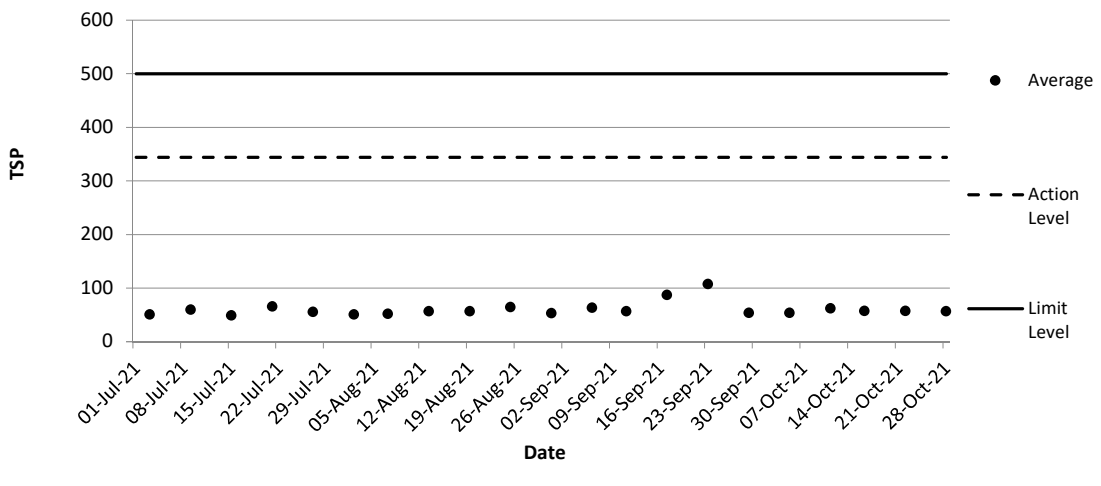

1-hr TSP Monitoring record for AMS 14

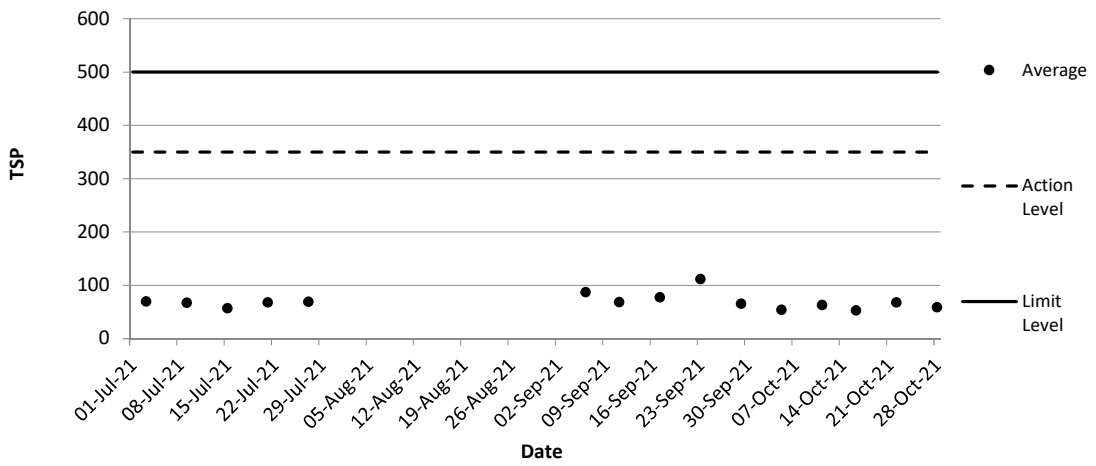

1-hr TSP Monitoring record for AMS 15

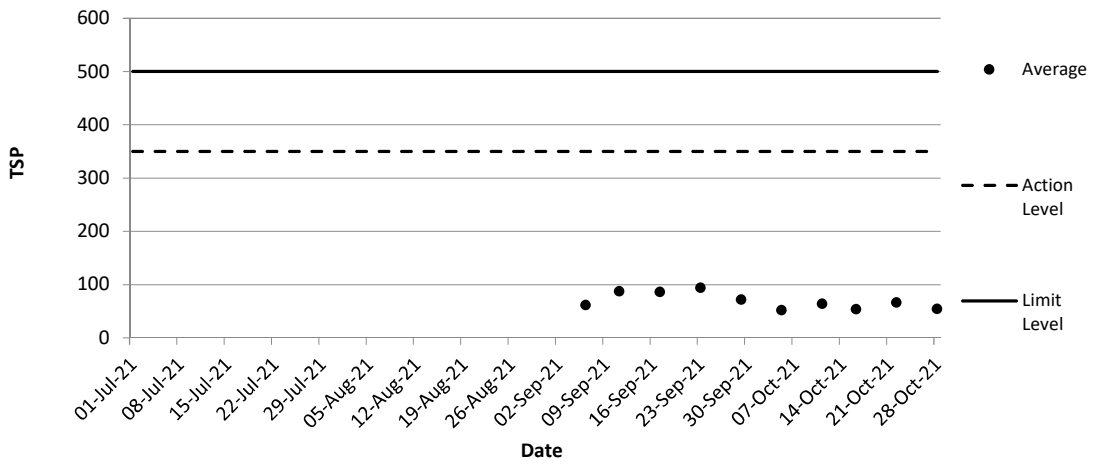

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AM55 - Tin Liu

Date and Time	TSP Concentration (µg/m³)
05/10/2021 07:05	53
05/10/2021 08:05	33
05/10/2021 09:05	38
05/10/2021 10:05	41
05/10/2021 11:05	42
05/10/2021 12:05	53
05/10/2021 13:05	58
05/10/2021 14:05	58
05/10/2021 15:05	53
05/10/2021 16:05	33
05/10/2021 17:05	36
05/10/2021 18:05	56
05/10/2021 19:05	33
05/10/2021 20:05	53
05/10/2021 21:05	55
05/10/2021 22:05	41
05/10/2021 23:05	48
06/10/2021 00:05	41
06/10/2021 01:05	52
06/10/2021 02:05	36
06/10/2021 03:05	53
06/10/2021 04:05	32
06/10/2021 05:05	52
06/10/2021 06:05	39
Average	45
Action Level	156
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
11/10/2021 07:00	50
11/10/2021 08:00	56
11/10/2021 09:00	48
11/10/2021 10:00	62
11/10/2021 11:00	53
11/10/2021 12:00	44
11/10/2021 13:00	59
11/10/2021 14:00	36
11/10/2021 15:00	67
11/10/2021 16:00	67
11/10/2021 17:00	47
11/10/2021 18:00	35
11/10/2021 19:00	41
11/10/2021 20:00	58
11/10/2021 21:00	48
11/10/2021 22:00	65
11/10/2021 23:00	44
12/10/2021 00:00	55
12/10/2021 01:00	65
12/10/2021 02:00	53
12/10/2021 03:00	59
12/10/2021 04:00	55
12/10/2021 05:00	61
12/10/2021 06:00	38
Average	53
Action Level	156
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
16/10/2021 07:16	56
16/10/2021 08:16	27
16/10/2021 09:16	29
16/10/2021 10:16	27
16/10/2021 11:16	41
16/10/2021 12:16	47
16/10/2021 13:16	44
16/10/2021 14:16	35
16/10/2021 15:16	26
16/10/2021 16:16	39
16/10/2021 17:16	29
16/10/2021 18:16	41
16/10/2021 19:16	56
16/10/2021 20:16	58
16/10/2021 21:16	29
16/10/2021 22:16	33
16/10/2021 23:16	50
17/10/2021 00:16	39
17/10/2021 01:16	58
17/10/2021 02:16	38
17/10/2021 03:16	48
17/10/2021 04:16	52
17/10/2021 05:16	32
17/10/2021 06:16	30
Average	40
Action Level	156
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
22/10/2021 08:40	40
22/10/2021 09:40	33
22/10/2021 10:40	33
22/10/2021 11:40	37
22/10/2021 12:40	38
22/10/2021 13:40	44
22/10/2021 14:40	52
22/10/2021 15:40	50
22/10/2021 16:40	58
22/10/2021 17:40	67
22/10/2021 18:40	73
22/10/2021 19:40	68
22/10/2021 20:40	58
22/10/2021 21:40	55
22/10/2021 22:40	53
22/10/2021 23:40	62
23/10/2021 00:40	61
23/10/2021 01:40	62
23/10/2021 02:40	62
23/10/2021 03:40	61
23/10/2021 04:40	58
23/10/2021 05:40	55
23/10/2021 06:40	53
23/10/2021 07:40	52
Average	54
Action Level	156
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
28/10/2021 07:20	50
28/10/2021 08:20	44
28/10/2021 09:20	36
28/10/2021 10:20	38
28/10/2021 11:20	64
28/10/2021 12:20	55
28/10/2021 13:20	58
28/10/2021 14:20	56
28/10/2021 15:20	41
28/10/2021 16:20	45
28/10/2021 17:20	42
28/10/2021 18:20	44
28/10/2021 19:20	45
28/10/2021 20:20	44
28/10/2021 21:20	36
28/10/2021 22:20	61
28/10/2021 23:20	47
29/10/2021 00:20	58
29/10/2021 01:20	45
29/10/2021 02:20	53
29/10/2021 03:20	44
29/10/2021 04:20	53
29/10/2021 05:20	50
29/10/2021 06:20	47
Average	48
Action Level	156
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS7A - Sheung Wo Che

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
05/10/2021 07:22	56
05/10/2021 08:22	29
05/10/2021 09:22	46
05/10/2021 10:22	56
05/10/2021 11:22	36
05/10/2021 12:22	56
05/10/2021 13:22	33
05/10/2021 14:22	48
05/10/2021 15:22	39
05/10/2021 16:22	53
05/10/2021 17:22	39
05/10/2021 18:22	54
05/10/2021 19:22	53
05/10/2021 20:22	53
05/10/2021 21:22	46
05/10/2021 22:22	56
05/10/2021 23:22	54
06/10/2021 00:22	45
06/10/2021 01:22	45
06/10/2021 02:22	34
06/10/2021 03:22	36
06/10/2021 04:22	34
06/10/2021 05:22	54
06/10/2021 06:22	40
Average	46
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
11/10/2021 07:16	54
11/10/2021 08:16	34
11/10/2021 09:16	62
11/10/2021 10:16	34
11/10/2021 11:16	50
11/10/2021 12:16	65
11/10/2021 13:16	43
11/10/2021 14:16	67
11/10/2021 15:16	62
11/10/2021 16:16	57
11/10/2021 17:16	37
11/10/2021 18:16	43
11/10/2021 19:16	39
11/10/2021 20:16	36
11/10/2021 21:16	46
11/10/2021 22:16	62
11/10/2021 23:16	33
12/10/2021 00:16	33
12/10/2021 01:16	54
12/10/2021 02:16	36
12/10/2021 03:16	36
12/10/2021 04:16	39
12/10/2021 05:16	36
12/10/2021 06:16	43
Average	46
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16/10/2021 07:33	64
16/10/2021 08:33	50
16/10/2021 09:33	57
16/10/2021 10:33	64
16/10/2021 11:33	50
16/10/2021 12:33	54
16/10/2021 13:33	50
16/10/2021 14:33	56
16/10/2021 15:33	53
16/10/2021 16:33	64
16/10/2021 17:33	36
16/10/2021 18:33	50
16/10/2021 19:33	43
16/10/2021 20:33	36
16/10/2021 21:33	46
16/10/2021 22:33	33
16/10/2021 23:33	53
17/10/2021 00:33	39
17/10/2021 01:33	34
17/10/2021 02:33	42
17/10/2021 03:33	48
17/10/2021 04:33	62
17/10/2021 05:33	33
17/10/2021 06:33	43
Average	48
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22/10/2021 08:54	26
22/10/2021 09:54	36
22/10/2021 10:54	37
22/10/2021 11:54	56
22/10/2021 12:54	51
22/10/2021 13:54	50
22/10/2021 14:54	54
22/10/2021 15:54	50
22/10/2021 16:54	51
22/10/2021 17:54	61
22/10/2021 18:54	57
22/10/2021 19:54	54
22/10/2021 20:54	57
22/10/2021 21:54	50
22/10/2021 22:54	28
22/10/2021 23:54	37
23/10/2021 00:54	37
23/10/2021 01:54	28
23/10/2021 02:54	25
23/10/2021 03:54	30
23/10/2021 04:54	34
23/10/2021 05:54	39
23/10/2021 06:54	42
23/10/2021 07:54	43
Average	43
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
28/10/2021 07:38	39
28/10/2021 08:38	57
28/10/2021 09:38	45
28/10/2021 10:38	34
28/10/2021 11:38	51
28/10/2021 12:38	34
28/10/2021 13:38	34
28/10/2021 14:38	51
28/10/2021 15:38	34
28/10/2021 16:38	60
28/10/2021 17:38	53
28/10/2021 18:38	56
28/10/2021 19:38	57
28/10/2021 20:38	42
28/10/2021 21:38	39
28/10/2021 22:38	48
28/10/2021 23:38	56
29/10/2021 00:38	51
29/10/2021 01:38	40
29/10/2021 02:38	43
29/10/2021 03:38	37
29/10/2021 04:38	42
29/10/2021 05:38	37
29/10/2021 06:38	59
Average	46
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS14 - Ha Wo Che

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
05/10/2021 07:41	42
05/10/2021 08:41	57
05/10/2021 09:41	56
05/10/2021 10:41	57
05/10/2021 11:41	48
05/10/2021 12:41	34
05/10/2021 13:41	37
05/10/2021 14:41	57
05/10/2021 15:41	53
05/10/2021 16:41	42
05/10/2021 17:41	51
05/10/2021 18:41	48
05/10/2021 19:41	53
05/10/2021 20:41	35
05/10/2021 21:41	32
05/10/2021 22:41	42
05/10/2021 23:41	46
06/10/2021 00:41	48
06/10/2021 01:41	54
06/10/2021 02:41	56
06/10/2021 03:41	37
06/10/2021 04:41	51
06/10/2021 05:41	32
06/10/2021 06:41	56
Average	47
Action Level	174
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
11/10/2021 07:32	62
11/10/2021 08:32	45
11/10/2021 09:32	48
11/10/2021 10:32	42
11/10/2021 11:32	46
11/10/2021 12:32	62
11/10/2021 13:32	64
11/10/2021 14:32	62
11/10/2021 15:32	42
11/10/2021 16:32	40
11/10/2021 17:32	42
11/10/2021 18:32	56
11/10/2021 19:32	53
11/10/2021 20:32	59
11/10/2021 21:32	54
11/10/2021 22:32	53
11/10/2021 23:32	40
12/10/2021 00:32	57
12/10/2021 01:32	64
12/10/2021 02:32	59
12/10/2021 03:32	62
12/10/2021 04:32	57
12/10/2021 05:32	56
12/10/2021 06:32	45
Average	53
Action Level	174
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16/10/2021 07:49	53
16/10/2021 08:49	48
16/10/2021 09:49	57
16/10/2021 10:49	50
16/10/2021 11:49	48
16/10/2021 12:49	46
16/10/2021 13:49	45
16/10/2021 14:49	46
16/10/2021 15:49	35
16/10/2021 16:49	50
16/10/2021 17:49	53
16/10/2021 18:49	50
16/10/2021 19:49	57
16/10/2021 20:49	46
16/10/2021 21:49	56
16/10/2021 22:49	37
16/10/2021 23:49	35
17/10/2021 00:49	42
17/10/2021 01:49	30
17/10/2021 02:49	56
17/10/2021 03:49	34
17/10/2021 04:49	38
17/10/2021 05:49	35
17/10/2021 06:49	42
Average	45
Action Level	174
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22/10/2021 09:16	38
22/10/2021 10:16	40
22/10/2021 11:16	45
22/10/2021 12:16	46
22/10/2021 13:16	58
22/10/2021 14:16	54
22/10/2021 15:16	62
22/10/2021 16:16	70
22/10/2021 17:16	67
22/10/2021 18:16	66
22/10/2021 19:16	64
22/10/2021 20:16	58
22/10/2021 21:16	50
22/10/2021 22:16	53
22/10/2021 23:16	51
23/10/2021 00:16	56
23/10/2021 01:16	58
23/10/2021 02:16	56
23/10/2021 03:16	46
23/10/2021 04:16	45
23/10/2021 05:16	42
23/10/2021 06:16	42
23/10/2021 07:16	37
23/10/2021 08:16	43
Average	52
Action Level	174
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
28/10/2021 07:52	42
28/10/2021 08:52	43
28/10/2021 09:52	56
28/10/2021 10:52	56
28/10/2021 11:52	45
28/10/2021 12:52	51
28/10/2021 13:52	53
28/10/2021 14:52	43
28/10/2021 15:52	42
28/10/2021 16:52	61
28/10/2021 17:52	64
28/10/2021 18:52	51
28/10/2021 19:52	57
28/10/2021 20:52	38
28/10/2021 21:52	56
28/10/2021 22:52	43
28/10/2021 23:52	38
29/10/2021 00:52	57
29/10/2021 01:52	39
29/10/2021 02:52	51
29/10/2021 03:52	43
29/10/2021 04:52	59
29/10/2021 05:52	46
29/10/2021 06:52	40
Average	49
Action Level	174
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 15 - Ha Wo Che

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
05/10/2021 07:55	56
05/10/2021 08:55	40
05/10/2021 09:55	44
05/10/2021 10:55	50
05/10/2021 11:55	40
05/10/2021 12:55	45
05/10/2021 13:55	42
05/10/2021 14:55	51
05/10/2021 15:55	62
05/10/2021 16:55	61
05/10/2021 17:55	40
05/10/2021 18:55	34
05/10/2021 19:55	36
05/10/2021 20:55	36
05/10/2021 21:55	61
05/10/2021 22:55	44
05/10/2021 23:55	47
06/10/2021 00:55	40
06/10/2021 01:55	50
06/10/2021 02:55	44
06/10/2021 03:55	37
06/10/2021 04:55	37
06/10/2021 05:55	37
06/10/2021 06:55	40
Average	45
Action Level	172
Limit Level	260



Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
11/10/2021 07:45	62
11/10/2021 08:45	39
11/10/2021 09:45	47
11/10/2021 10:45	48
11/10/2021 11:45	61
11/10/2021 12:45	53
11/10/2021 13:45	48
11/10/2021 14:45	34
11/10/2021 15:45	54
11/10/2021 16:45	34
11/10/2021 17:45	64
11/10/2021 18:45	65
11/10/2021 19:45	62
11/10/2021 20:45	40
11/10/2021 21:45	67
11/10/2021 22:45	45
11/10/2021 23:45	51
12/10/2021 00:45	56
12/10/2021 01:45	51
12/10/2021 02:45	36
12/10/2021 03:45	59
12/10/2021 04:45	61
12/10/2021 05:45	36
12/10/2021 06:45	44
Average	51
Action Level	172
Limit Level	260



Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16/10/2021 08:02	54
16/10/2021 09:02	39
16/10/2021 10:02	53
16/10/2021 11:02	33
16/10/2021 12:02	42
16/10/2021 13:02	34
16/10/2021 14:02	37
16/10/2021 15:02	51
16/10/2021 16:02	56
16/10/2021 17:02	54
16/10/2021 18:02	45
16/10/2021 19:02	51
16/10/2021 20:02	51
16/10/2021 21:02	42
16/10/2021 22:02	44
16/10/2021 23:02	36
17/10/2021 00:02	59
17/10/2021 01:02	31
17/10/2021 02:02	39
17/10/2021 03:02	44
17/10/2021 04:02	51
17/10/2021 05:02	54
17/10/2021 06:02	61
17/10/2021 07:02	31
Average	46
Action Level	172
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22/10/2021 09:24	45
22/10/2021 10:24	50
22/10/2021 11:24	58
22/10/2021 12:24	64
22/10/2021 13:24	69
22/10/2021 14:24	66
22/10/2021 15:24	55
22/10/2021 16:24	48
22/10/2021 17:24	44
22/10/2021 18:24	42
22/10/2021 19:24	37
22/10/2021 20:24	39
22/10/2021 21:24	39
22/10/2021 22:24	44
22/10/2021 23:24	41
23/10/2021 00:24	33
23/10/2021 01:24	36
23/10/2021 02:24	34
23/10/2021 03:24	36
23/10/2021 04:24	41
23/10/2021 05:24	44
23/10/2021 06:24	39
23/10/2021 07:24	47
23/10/2021 08:24	37
Average	45
Action Level	172
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
28/10/2021 08:03	57
28/10/2021 09:03	34
28/10/2021 10:03	56
28/10/2021 11:03	50
28/10/2021 12:03	36
28/10/2021 13:03	33
28/10/2021 14:03	44
28/10/2021 15:03	57
28/10/2021 16:03	42
28/10/2021 17:03	51
28/10/2021 18:03	57
28/10/2021 19:03	54
28/10/2021 20:03	40
28/10/2021 21:03	39
28/10/2021 22:03	48
28/10/2021 23:03	51
29/10/2021 00:03	57
29/10/2021 01:03	48
29/10/2021 02:03	36
29/10/2021 03:03	57
29/10/2021 04:03	44
29/10/2021 05:03	31
29/10/2021 06:03	47
29/10/2021 07:03	56
Average	47
Action Level	172
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

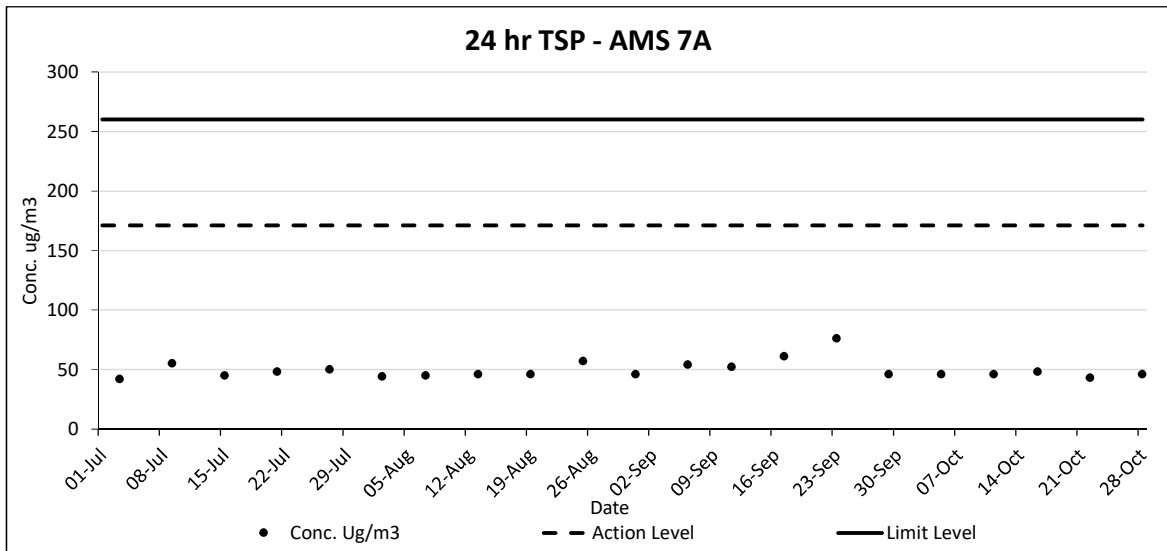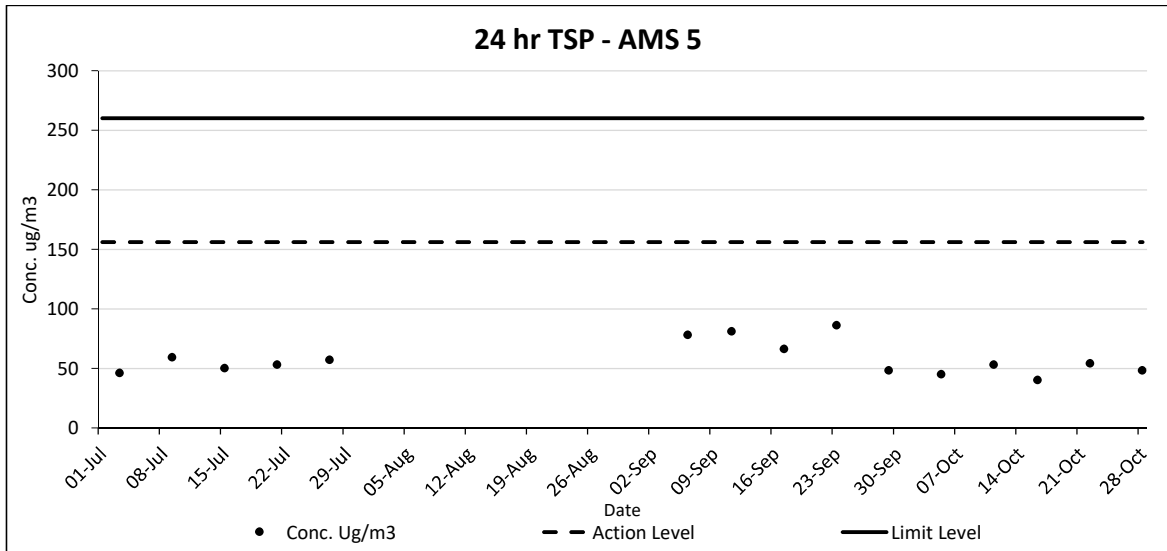

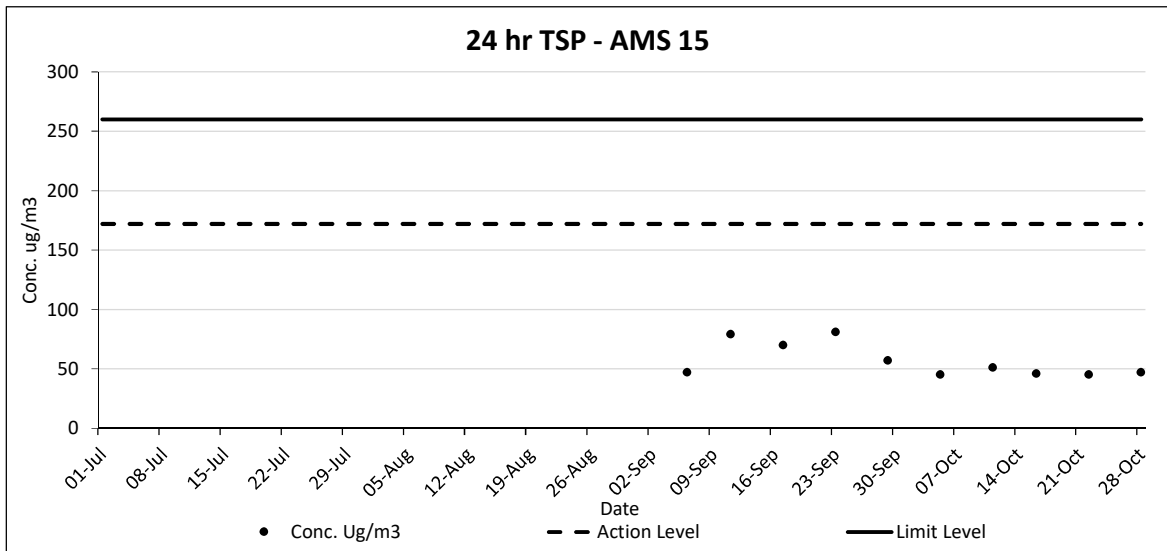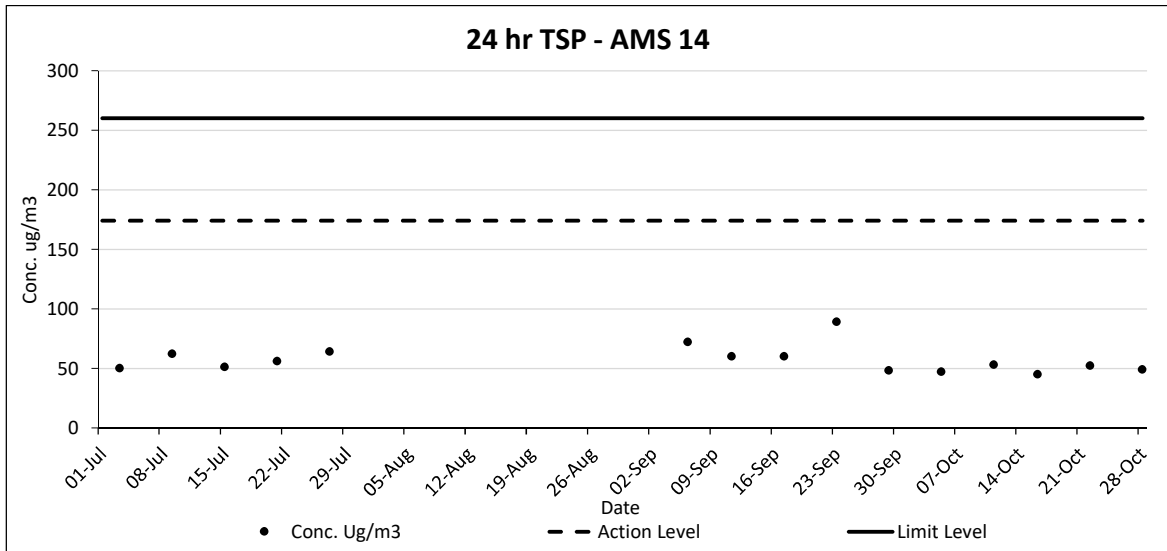

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix G

Noise Monitoring Data

Impact Noise Monitoring Result for NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

NMS 1 Scenery Court

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	13:00	65.2	63.0	66.5	75	65.2	Fine	0.5
11-Oct-21	11:17	66.1	63.5	68.5		66.1	Fine	0.6
22-Oct-21	13:22	67.3	64.5	69.0		67.3	Fine	0.5
28-Oct-21	16:59	63.9	61.5	65.0		63.9	Fine	0.4

NMS 2 Villa Le Parc

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	08:31	54.2	51.5	56.0	75	54.2	Fine	0.7
11-Oct-21	08:20	53.3	51.0	55.0		53.3	Fine	0.8
22-Oct-21	08:32	53.7	51.5	54.5		53.7	Fine	1.1
28-Oct-21	08:30	53.4	52.0	54.5		53.4	Fine	0.8

NMS 3 Hilton Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	10:30	68.0	65.0	70.0	75	68.0	Fine	1.3
11-Oct-21	10:06	67.9	65.0	70.0		67.9	Fine	1.1
22-Oct-21	10:19	67.9	64.5	69.0		67.9	Fine	0.6
28-Oct-21	16:18	68.2	65.5	69.5		68.2	Fine	0.9

NMS 4 Tin Liu

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	09:14	65.5	62.0	66.5	75	65.5	Fine	0.9
11-Oct-21	08:48	64.8	62.5	66.0		64.8	Fine	0.9
22-Oct-21	09:09	65.0	62.5	67.0		65.0	Fine	1.0
28-Oct-21	09:08	64.8	62.0	66.0		64.8	Fine	0.6

NMS 5A Wai Wah Centre

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	11:04	70.0	67.0	72.0	75	70.0	Fine	0.8
11-Oct-21	10:39	69.5	68.0	70.5		69.5	Fine	1.0
22-Oct-21	10:53	69.3	67.0	70.5		69.3	Fine	0.8
28-Oct-21	15:44	69.5	66.0	71.0		69.5	Fine	0.8

NMS 6A Wai Wah Centre

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	13:40	72.8	69.5	74.0	75	72.8	Fine	1.1
11-Oct-21	13:09	73.3	70.5	75.5		73.3	Fine	1.6
22-Oct-21	11:29	72.2	69.5	73.5		72.2	Fine	1.2
28-Oct-21	15:08	71.3	67.0	74.5		71.3	Fine	1.0

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 7 Tin Liu

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-Oct-21	09:48	65.3	62.5	66.5	75	65.3	Fine	0.7
11-Oct-21	09:30	64.6	62.0	67.0		64.6	Fine	0.5
22-Oct-21	09:43	64.4	63.0	66.0		64.4	Fine	1.1
28-Oct-21	09:42	64.7	62.5	67.0		64.7	Fine	1.0

NMS 8 Shatin Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	08:43	65.4	63.0	66.5	75	65.4	Fine	1.3
12-Oct-21	15:30	66.4	65.0	67.5		66.4	Fine	1.5
23-Oct-21	08:20	69.7	66.5	72.0		69.7	Fine	0.7
29-Oct-21	15:57	67.8	66.5	69.0		67.8	Fine	0.8

NMS 9 Lek Yuen Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	10:05	67.3	63.5	69.0	75	67.3	Fine	0.8
12-Oct-21	07:55	69.8	65.0	71.5		69.8	Fine	1.1
23-Oct-21	09:44	70.3	66.5	74.0		70.3	Fine	1.1
29-Oct-21	14:09	66.0	63.0	67.0		66.0	Fine	0.5

NMS 10A Shatin Tsung Tsin School

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	10:40	63.6	60.5	66.0	70	63.6	Fine	0.7
12-Oct-21	08:30	64.0	61.0	66.0		64.0	Fine	1.0
23-Oct-21	10:22	62.6	60.5	64.0		62.6	Fine	0.7
29-Oct-21	13:02	65.4	61.5	66.0		65.4	Fine	0.8

*Note: The school calendar was provide in Appendix E.

NMS 11 Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	16:57	61.5	58.5	63.0	75	61.5	Fine	0.7
12-Oct-21	14:16	60.0	56.5	61.0		60.0	Fine	1.0
23-Oct-21	16:16	62.2	60.0	64.5		62.2	Fine	0.7
29-Oct-21	11:08	64.6	61.5	66.5		64.6	Fine	0.7

NMS 12 SKH Holy Spirit Primary School

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	11:16	64.8	62.0	66.5	70	64.8	Fine	1.1
12-Oct-21	09:03	63.1	60.0	65.0		63.1	Fine	1.3
23-Oct-21	11:00	63.4	61.0	66.0		63.4	Fine	0.7
29-Oct-21	13:35	63.2	61.0	65.0	65	63.2	Fine	0.9

For SKH Holy Spirit Primary School, 70 dB(A) noise level is set for school for normal days. The examination period began on 26th to 29th October 2021. Hence, the daytime noise level changed from 70 to 65 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 13 Lek Yuen Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
06-Oct-21	13:07	59.0	55.5	61.0	75	59.0	Fine	0.6
12-Oct-21	09:40	60.9	57.0	63.5		60.9	Fine	0.7
23-Oct-21	11:38	66.8	63.5	68.0		66.8	Fine	0.6
29-Oct-21	11:43	61.5	59.5	63.0		61.5	Fine	0.9

NMS 14 Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
06-Oct-21	16:18	63.0	59.5	65.0	75	63.0	Fine	1.0
12-Oct-21	13:39	61.6	58.0	62.5		61.6	Fine	1.0
23-Oct-21	15:40	64.0	61.0	66.3		64.0	Fine	0.6
29-Oct-21	10:35	63.4	61.0	65.0		63.4	Fine	0.7

NMS 15 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	15:00	60.9	58.0	62.0	75	60.9	Fine	1.2
11-Oct-21	14:28	59.0	54.5	61.0		59.0	Fine	1.3
22-Oct-21	09:24	61.2	58.0	62.5		61.2	Fine	0.9
28-Oct-21	11:05	62.5	59.0	63.5		62.5	Fine	0.7

NMS 16 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	15:37	63.0	60.0	64.5	75	63.0	Fine	1.2
11-Oct-21	15:05	62.5	58.5	64.0		62.5	Fine	1.0
22-Oct-21	10:03	62.1	59.5	63.5		62.1	Fine	0.9
28-Oct-21	13:00	61.0	58.5	63.0		61.0	Fine	1.1

NMS 17 Shatin Pui Ying College

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
06-Oct-21	13:50	63.1	60.0	66.0	70	63.1	Fine	1.4
12-Oct-21	10:18	64.8	62.0	68.0		64.8	Fine	1.1
23-Oct-21	14:58	61.8	60.0	63.5	65	61.8	Fine	0.6
29-Oct-21	09:22	64.5	61.5	65.0		64.5	Fine	0.8

For Shatin Pui Ying College, 70 dB(A) noise level is set for school for normal days. The examination period began on 25th to 29th October 2021. Hence, the daytime noise level changed from 70 to 65 dB(A).

NMS 18 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-Oct-21	16:15	61.8	59.5	62.5	75	61.8	Fine	1.0
11-Oct-21	15:38	60.7	56.0	62.5		60.7	Fine	1.2
22-Oct-21	10:35	59.1	56.5	61.0		59.1	Fine	0.4
28-Oct-21	13:33	60.6	57.0	61.5		60.6	Fine	1.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 19 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	14:28	66.5	65.0	68.0	75	66.5	Fine	0.9
12-Oct-21	10:55	63.3	61.5	65.0		63.3	Fine	0.8
23-Oct-21	13:38	67.9	65.0	70.3		67.9	Fine	0.8
29-Oct-21	08:48	63.1	61.5	65.0		63.1	Fine	0.7

NMS 20 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	15:00	64.1	60.5	65.5	75	64.1	Fine	0.9
12-Oct-21	11:29	62.9	61.0	64.0		62.9	Fine	0.5
23-Oct-21	14:15	66.8	64.5	69.0		66.8	Fine	1.1
29-Oct-21	08:11	61.1	59.0	63.0		61.1	Fine	0.6

NMS 23 Pai Tau

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-Oct-21	14:18	64.7	61.5	66.0	75	64.7	Fine	0.6
11-Oct-21	13:45	66.9	62.0	68.0		66.9	Fine	0.6
22-Oct-21	08:48	66.6	62.5	68.5		66.6	Fine	0.6
28-Oct-21	10:24	65.7	62.0	67.0		65.7	Fine	0.5

NMS 24 Shatin Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	09:26	64.5	62.0	66.0	75	64.5	Fine	1.5
12-Oct-21	16:04	63.0	61.5	64.5		63.0	Fine	1.0
23-Oct-21	08:56	68.9	66.0	71.5		68.9	Fine	0.7
29-Oct-21	15:22	68.6	66.0	70.0		68.6	Fine	0.7

NMS 25A Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	17:13	60.0	56.0	61.5	75	60.0	Fine	0.8
12-Oct-21	14:53	58.9	55.0	60.0		58.9	Fine	0.7
23-Oct-21	16:52	70.4	66.0	73.0		70.4	Fine	0.4
29-Oct-21	14:44	64.0	62.5	66.0		64.0	Fine	0.8

NMS 26 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
06-Oct-21	15:41	68.9	62.5	71.0	75	68.9	Fine	0.5
12-Oct-21	13:02	63.5	60.0	65.0		63.5	Fine	0.6
23-Oct-21	13:00	72.4	68.5	75.5		72.4	Fine	1.3
29-Oct-21	09:58	69.4	67.0	91.5		69.4	Fine	0.9







NMS 27 Jockey Club Ti-I College







Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-Oct-21	17:11	65.4	63.5	67.0	70	65.4	Fine	0.6
11-Oct-21	16:30	64.0	62.0	66.0		64.0	Fine	1.4
22-Oct-21	11:28	63.7	60.5	65.5		63.7	Fine	1.0
28-Oct-21	14:19	64.2	61.0	66.5		64.2	Fine	1.3







*Note: The school calendar was provide in Appendix E.








If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

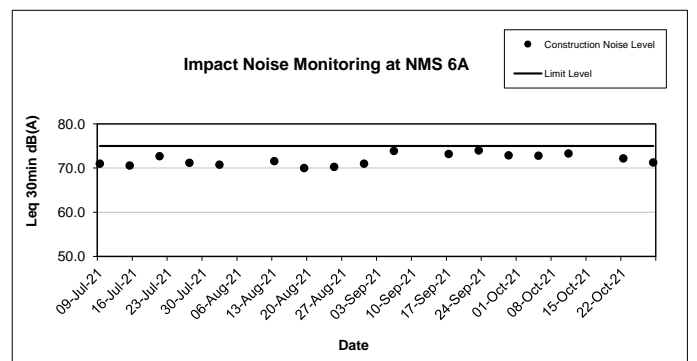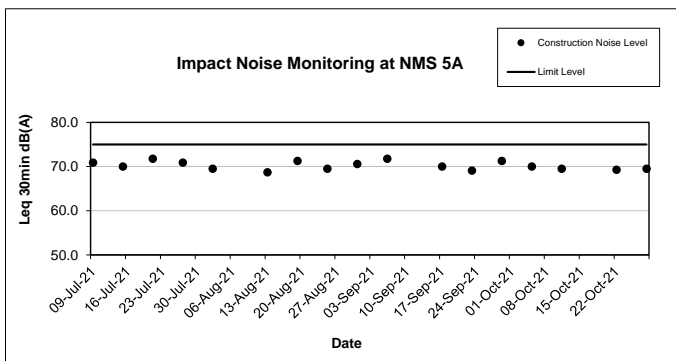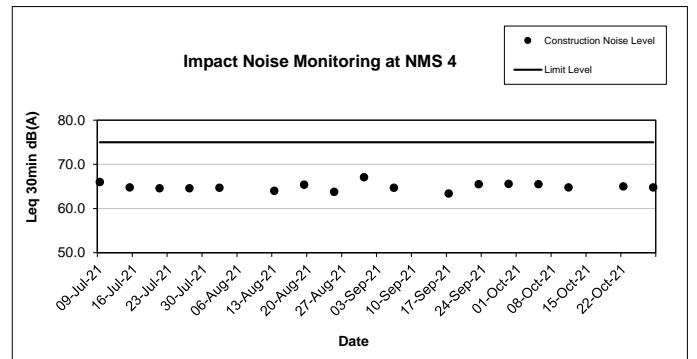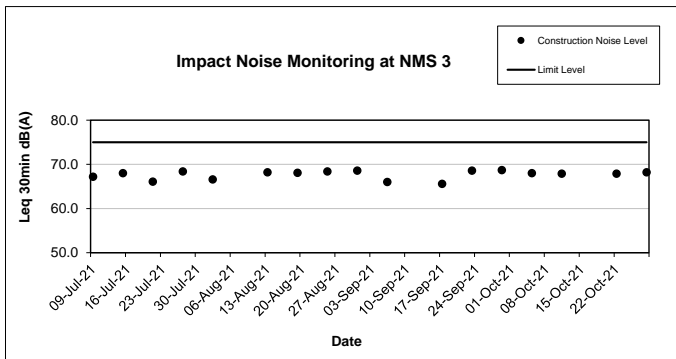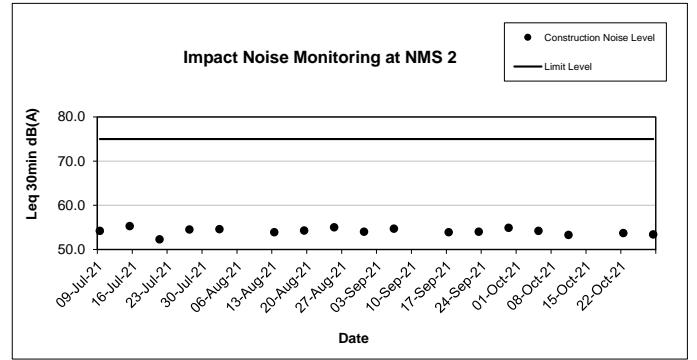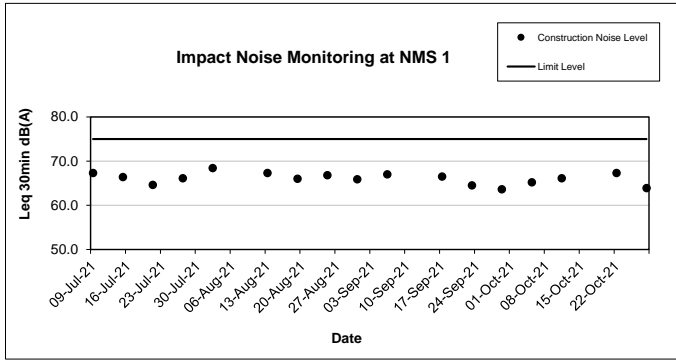

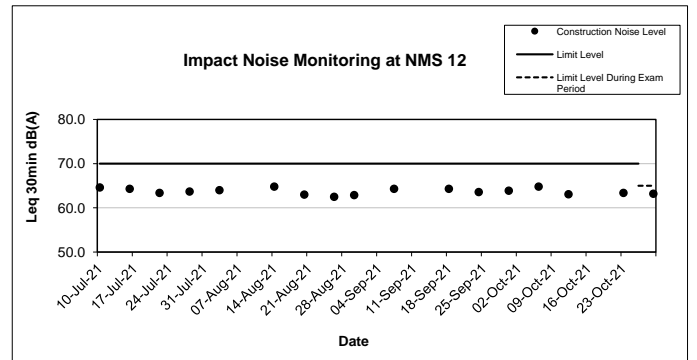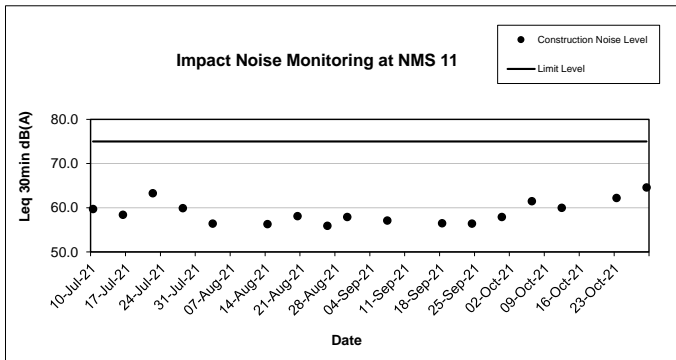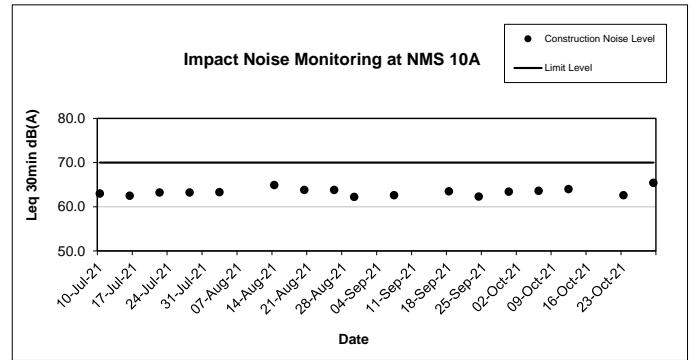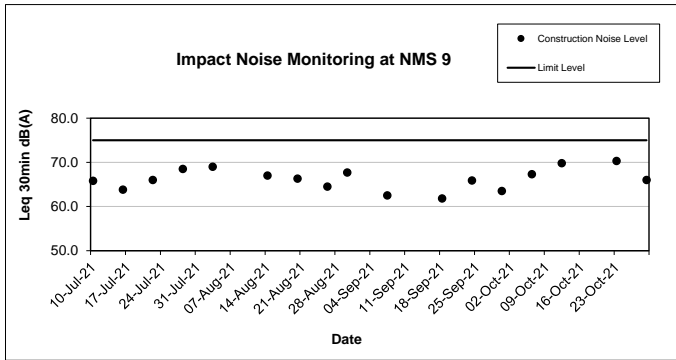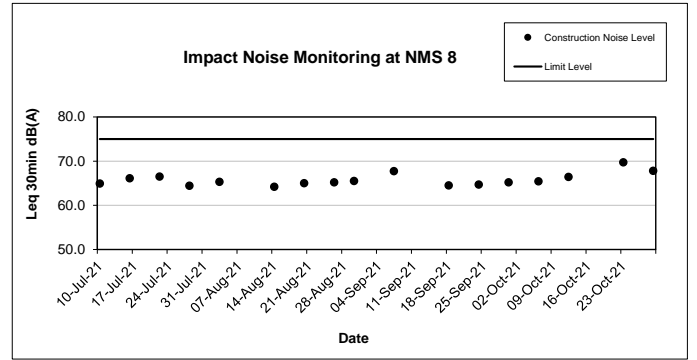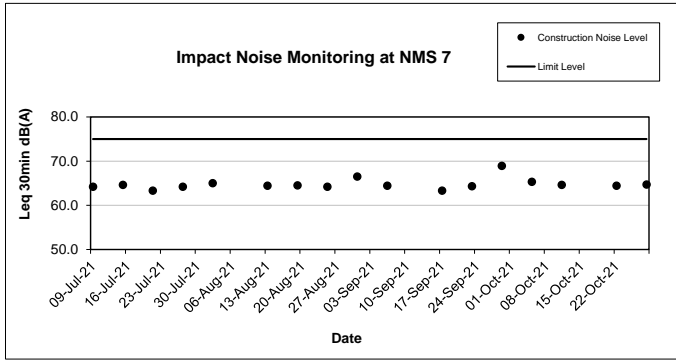

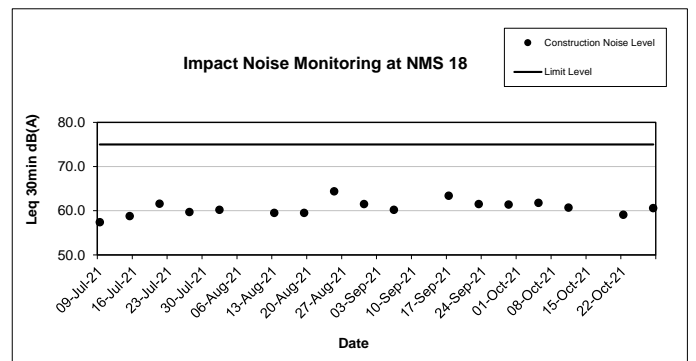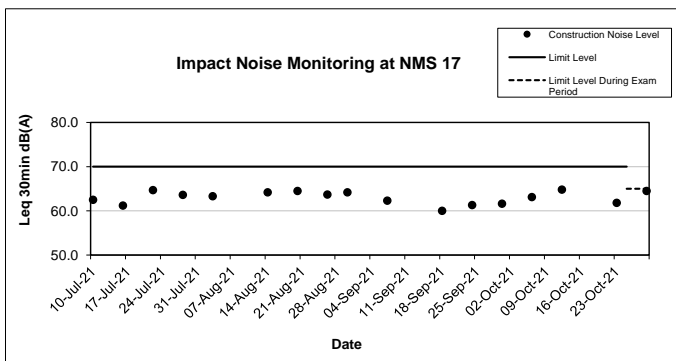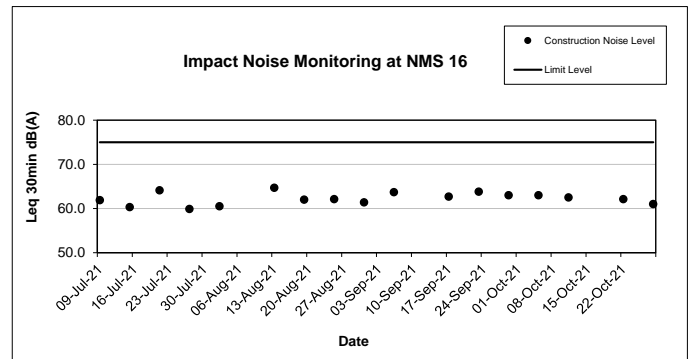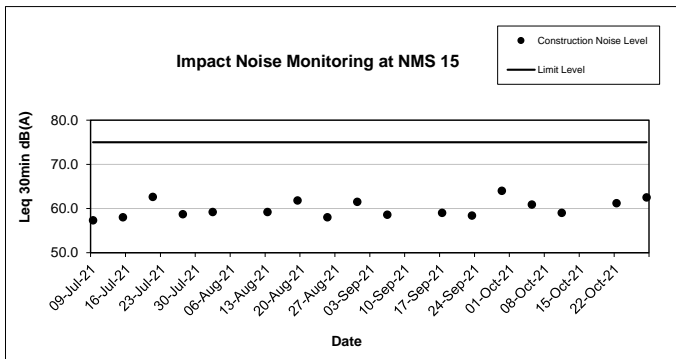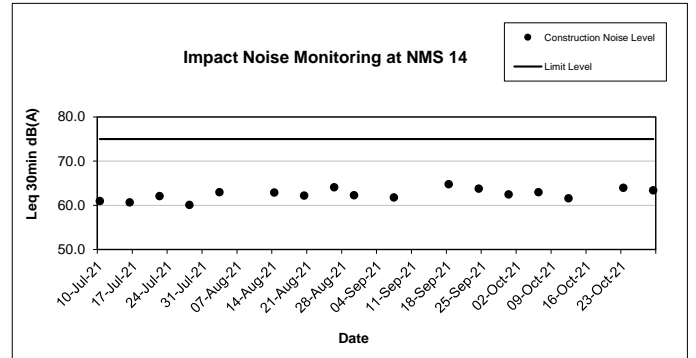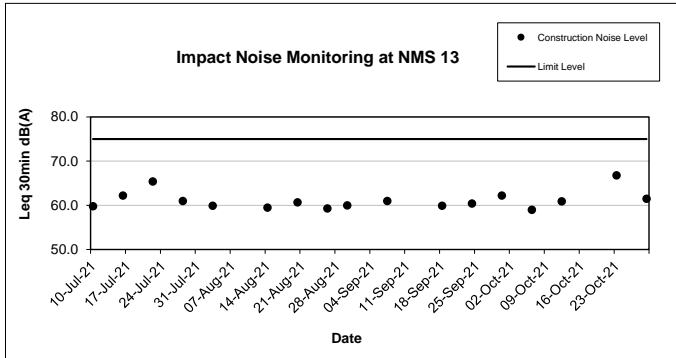

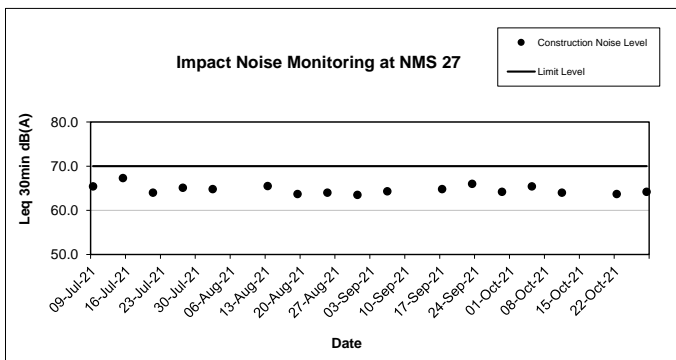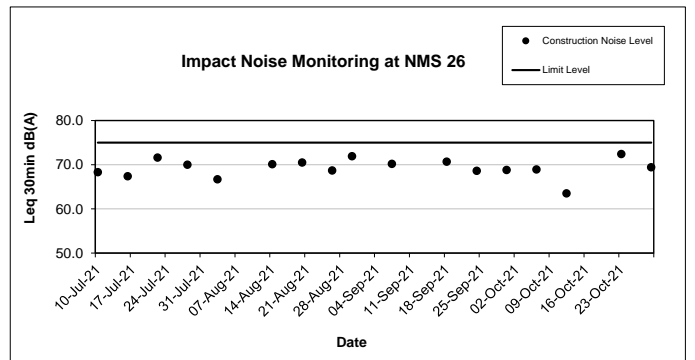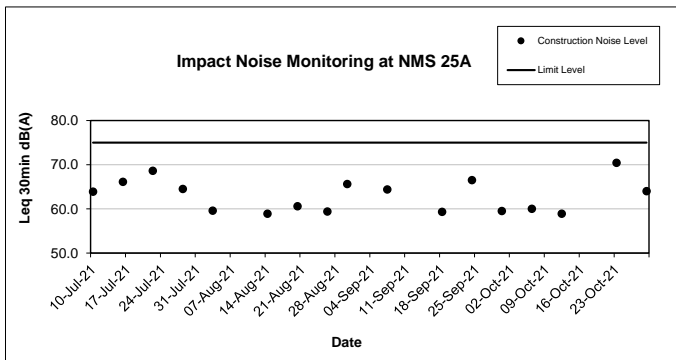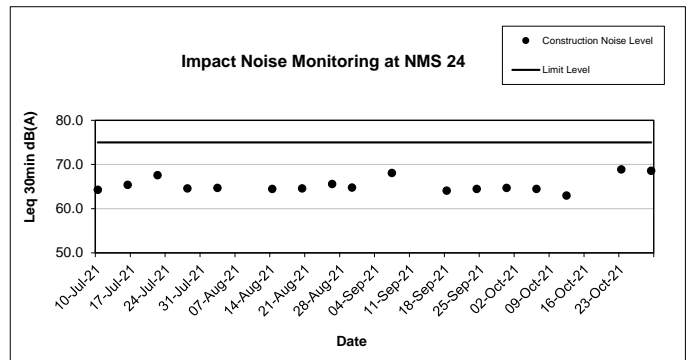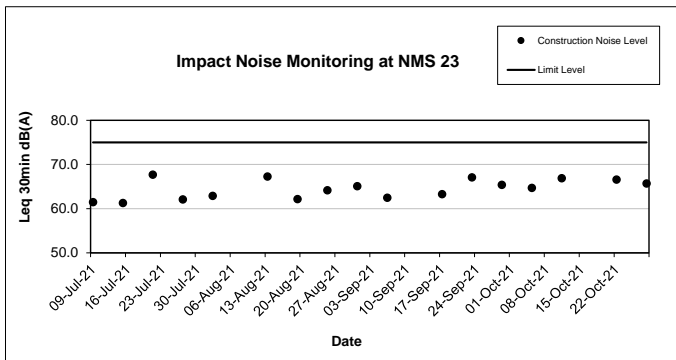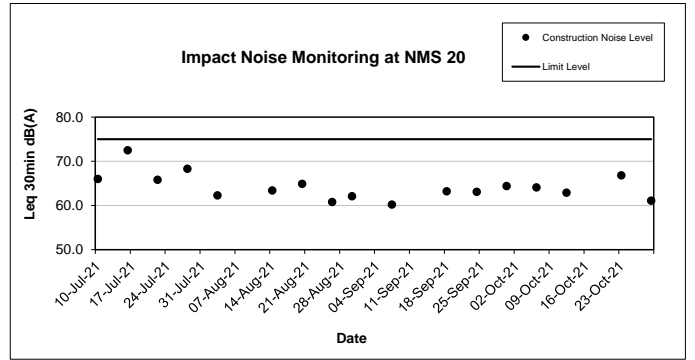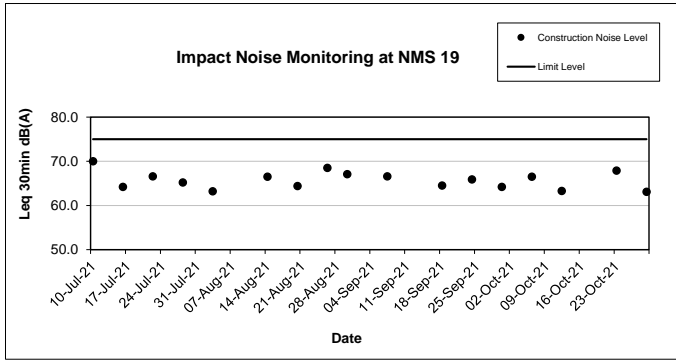

Night Time Noise Monitoring Result for NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

NMS 1 Scenery Court

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:00	58.1	61.4	52.8 - 66.3	55	Measured Noise Level<Baseline	Overcast	0.5
11-Oct-21	23:00	58.5				Measured Noise Level<Baseline	Overcast	2.5
21-Oct-21	23:00	59.0				Measured Noise Level<Baseline	Fine	0.8
28-Oct-21	23:00	59.9				Measured Noise Level<Baseline	Fine	0.7

NMS 2 Villa Le Parc

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	03:16	51.8	49.7	40.1 - 58.2	55	Measured Noise Level<Limit Level	Overcast	1.2
11-Oct-21	23:03	53.0				Measured Noise Level<Limit Level	Overcast	2.9
21-Oct-21	23:00	53.7				Measured Noise Level<Limit Level	Fine	0.6
28-Oct-21	23:00	50.7				Measured Noise Level<Limit Level	Fine	0.6

NMS 3 Hilton Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:21	68.8	70.9	60.2 - 78.9	55	Measured Noise Level<Baseline	Overcast	0.4
11-Oct-21	23:22	66.1				Measured Noise Level<Baseline	Overcast	1.8
21-Oct-21	23:22	63.0				Measured Noise Level<Baseline	Fine	0.7
28-Oct-21	23:21	60.9				Measured Noise Level<Baseline	Fine	0.6

NMS 4 Tin Liu

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	02:45	60.4	62.6	53.1 - 68.1	55	Measured Noise Level<Baseline	Overcast	0.6
11-Oct-21	23:29	60.4				Measured Noise Level<Baseline	Overcast	2.8
21-Oct-21	23:26	61.2				Measured Noise Level<Baseline	Fine	0.8
28-Oct-21	23:27	61.1				Measured Noise Level<Baseline	Fine	0.4

NMS 5A Wai Wah Centre

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:40	68.0	67.9	62.0 - 75.2	55	51.6*	Overcast	0.8
11-Oct-21	23:43	64.8				Measured Noise Level<Baseline	Overcast	2.2
21-Oct-21	23:40	68.0				51.6*	Fine	0.9
28-Oct-21	23:44	69.6				64.7**	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

**Exceedance due to traffic vehicle noise

NMS 6A Wai Wah Centre

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:58	69.5	71.5	65.0 - 85.9	55	Measured Noise Level<Baseline	Overcast	0.9
12-Oct-21	00:04	63.2				Measured Noise Level<Baseline	Overcast	2.4
21-Oct-21	23:58	68.8				Measured Noise Level<Baseline	Fine	0.6
29-Oct-21	00:18	71.3				Measured Noise Level<Baseline	Fine	0.9

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 7 Tin Liu

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	02:23	59.2	59.0	51.4 - 65.5	55	45.7*	Overcast	0.5
11-Oct-21	23:49	59.4				48.8*	Overcast	1.5
21-Oct-21	23:48	59.4				48.8*	Fine	1.1
28-Oct-21	23:48	60.2				54.0*	Fine	0.7

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 8 Shatin Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	00:24	61.3	64.4	55.6 - 72.8	55	Measured Noise Level<Baseline	Overcast	0.9
12-Oct-21	00:28	62.0				Measured Noise Level<Baseline	Overcast	2.0
22-Oct-21	00:23	61.2				Measured Noise Level<Baseline	Fine	1.0
29-Oct-21	00:42	62.8				Measured Noise Level<Baseline	Fine	0.7

NMS 9 Lek Yuen Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	01:11	56.8	53.5	39.5 - 63.1	55	54.1*	Overcast	1.2
12-Oct-21	00:55	55.3				50.6*	Overcast	2.8
22-Oct-21	01:10	57.0				54.4*	Fine	0.8
29-Oct-21	01:26	52.9				Measured Noise Level<Limit Level	Fine	0.9

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 11 Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	01:10	56.8	53.2	46.1 - 62.8	55	54.3*	Overcast	0.6
12-Oct-21	01:00	53.6				Measured Noise Level<Limit Level	Overcast	0.6
22-Oct-21	00:50	53.1				Measured Noise Level<Limit Level	Fine	0.6
29-Oct-21	00:53	49.1				Measured Noise Level<Limit Level	Fine	0.3

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 13 Lek Yuen Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	01:41	57.8	57.3	45.4 - 72.5	55	48.2*	Overcast	0.9
12-Oct-21	01:17	56.5				Measured Noise Level<Baseline	Overcast	2.6
22-Oct-21	01:38	54.5				Measured Noise Level<Limit Level	Fine	0.8
29-Oct-21	01:49	54.9				Measured Noise Level<Limit Level	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 14 Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	00:49	57.3	54.1	46.1 - 62.8	55	54.5*	Overcast	1.5
12-Oct-21	01:27	55.3				49.1*	Overcast	2.5
22-Oct-21	01:13	54.6				Measured Noise Level<Limit Level	Fine	0.7
29-Oct-21	01:12	53.2				Measured Noise Level<Limit Level	Fine	1.1

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 15 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	00:26	57.8	58.8	48.4 - 69.7	55	Measured Noise Level<Baseline	Overcast	1.2
12-Oct-21	01:54	58.0				Measured Noise Level<Baseline	Overcast	3.4
22-Oct-21	01:40	56.6				Measured Noise Level<Baseline	Fine	0.6
29-Oct-21	01:32	56.8				Measured Noise Level<Baseline	Fine	0.4

NMS 16 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	00:02	59.7	60.1	51.4 - 69.5	55	Measured Noise Level<Baseline	Overcast	1.2
12-Oct-21	02:15	56.7				Measured Noise Level<Baseline	Overcast	3.6
19-Aug-21	23:19	57.7				Measured Noise Level<Baseline	Fine	0.7
29-Oct-21	01:56	54.8				Measured Noise Level<Limit Level	Fine	0.8

NMS 18 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:44	59.2	63.2	56.0 - 72.1	55	Measured Noise Level<Baseline	Overcast	1.2
12-Oct-21	02:33	58.4				Measured Noise Level<Baseline	Overcast	2.8
22-Oct-21	01:59	55.8				Measured Noise Level<Baseline	Fine	1.2
29-Oct-21	02:13	55.3				Measured Noise Level<Baseline	Fine	0.8

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 19 Wo Che Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	02:06	62.0	61.7	53.8 - 72.8	55	50.2*	Overcast	1.0
12-Oct-21	01:40	57.3				Measured Noise Level<Baseline	Overcast	2.2
22-Oct-21	02:04	61.4				Measured Noise Level<Baseline	Fine	0.9
29-Oct-21	02:15	61.6				Measured Noise Level<Baseline	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 20 Wo Che Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	02:26	57.9	57.7	48.6 - 71.7	55	44.4*	Overcast	0.7
12-Oct-21	02:01	53.9				Measured Noise Level<Limit Level	Overcast	2.7
22-Oct-21	02:24	54.0				Measured Noise Level<Limit Level	Fine	0.7
29-Oct-21	02:33	55.3				Measured Noise Level<Baseline	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 23 Pai Tau

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	01:59	60.5	59.9	47.8 - 69.8	55	51.6*	Overcast	1.3
12-Oct-21	00:22	59.7				Measured Noise Level<Baseline	Overcast	2.1
22-Oct-21	00:09	61.2				55.3*	Fine	1.0
29-Oct-21	00:15	60.2				48.4*	Fine	0.3

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 24 Shatin Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	00:43	58.4	58.0	50.2 - 66.7	55	47.8*	Overcast	0.9
12-Oct-21	02:31	54.7				Measured Noise Level<Limit Level	Overcast	2.8
22-Oct-21	00:42	58.3				46.5*	Fine	0.8
29-Oct-21	01:00	58.6				49.7*	Fine	0.6

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 25A Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
08-Oct-21	01:38	59.8	59.7	50.3 - 68.4	55	43.4*	Overcast	1.0
12-Oct-21	00:42	54.2				Measured Noise Level<Limit Level	Overcast	3.1
22-Oct-21	00:29	56.0				Measured Noise Level<Baseline	Fine	0.7
29-Oct-21	00:36	51.8				Measured Noise Level<Limit Level	Fine	0.4

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).





NMS 26 Wo Che Estate





Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
07-Oct-21	23:21	61.7	61.2	45.7 - 70.1	55	52.1*	Overcast	1.6
12-Oct-21	03:02	60.6				Measured Noise Level<Baseline	Overcast	2.3
22-Oct-21	02:54	60.6				Measured Noise Level<Baseline	Fine	0.5
29-Oct-21	02:38	61.7				52.1*	Fine	0.6





Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).





If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:






$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

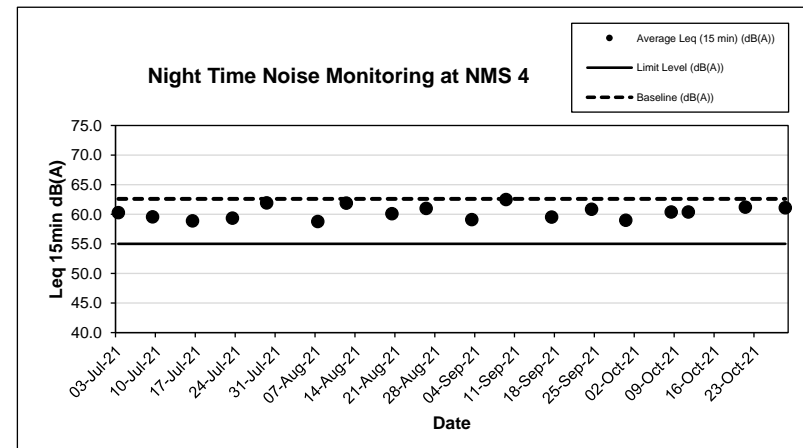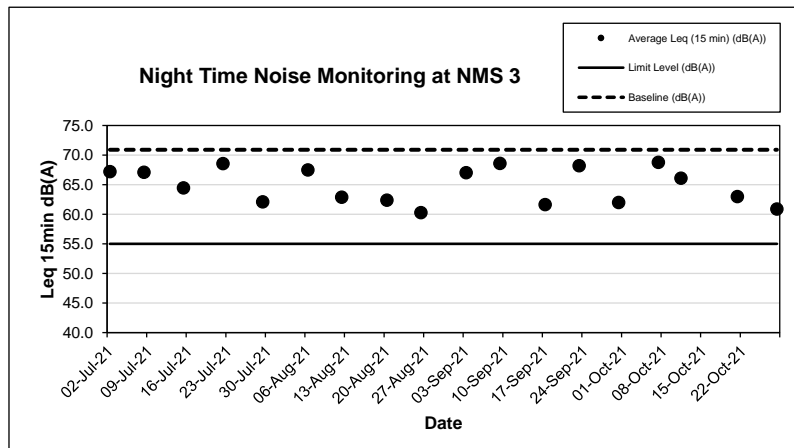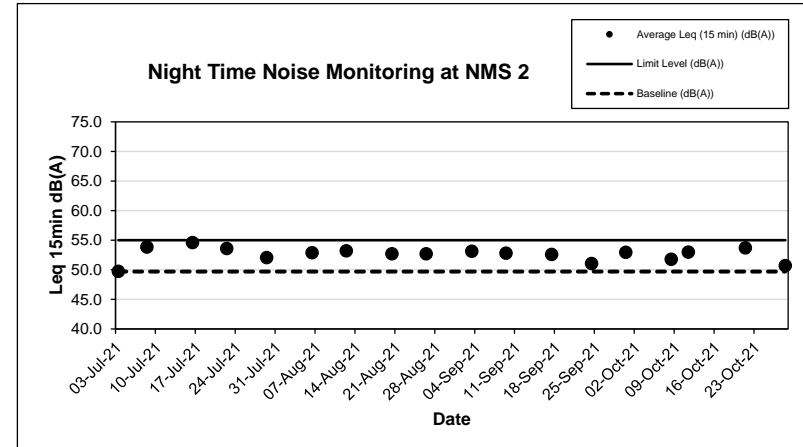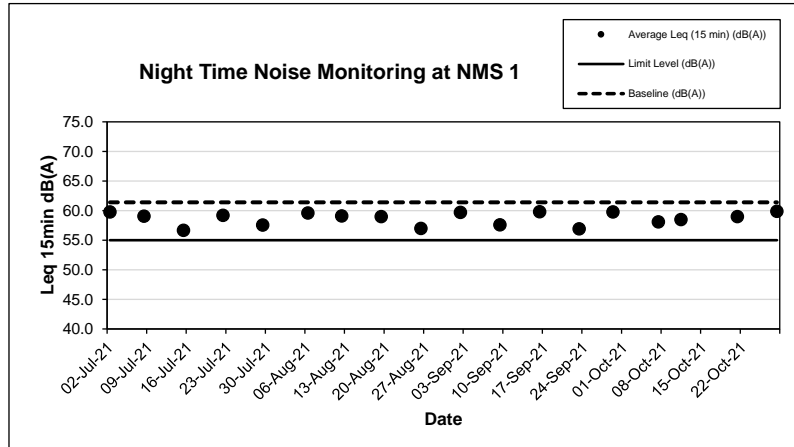

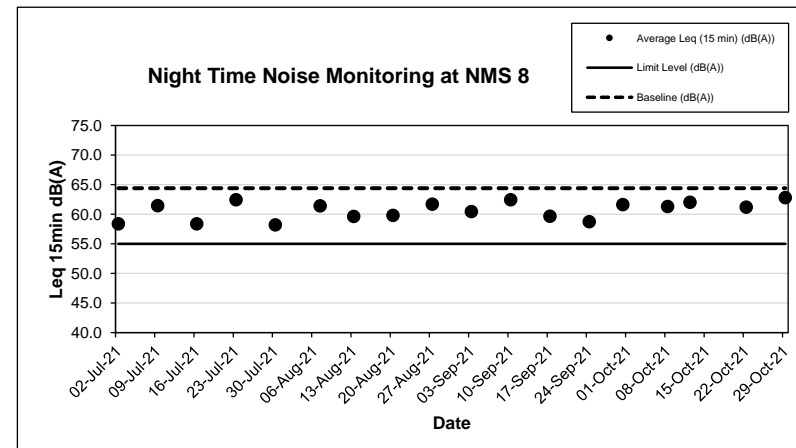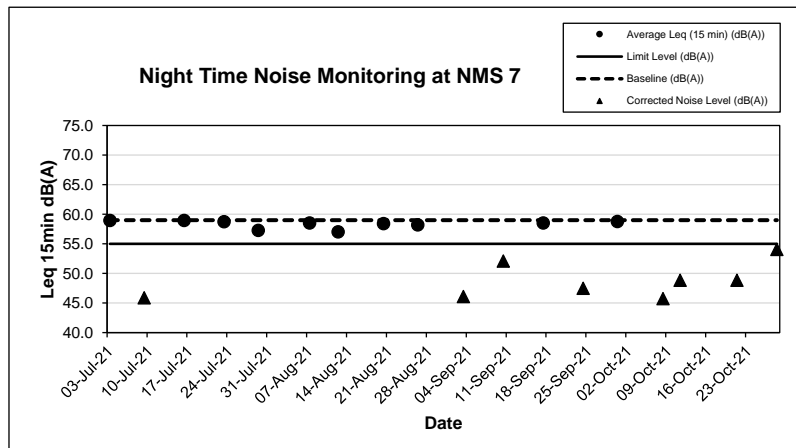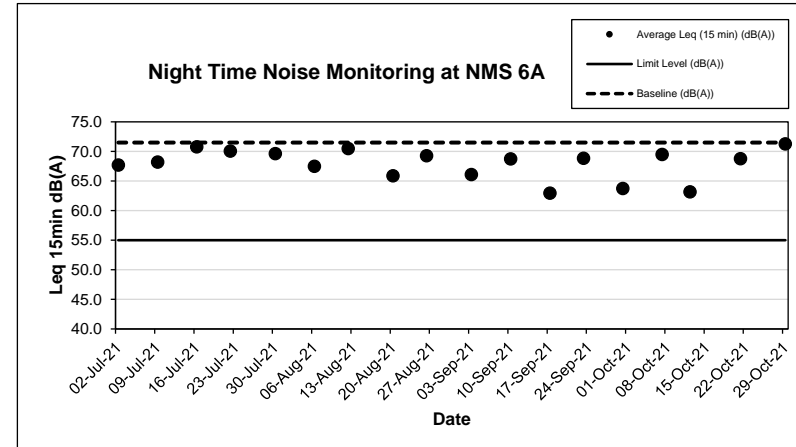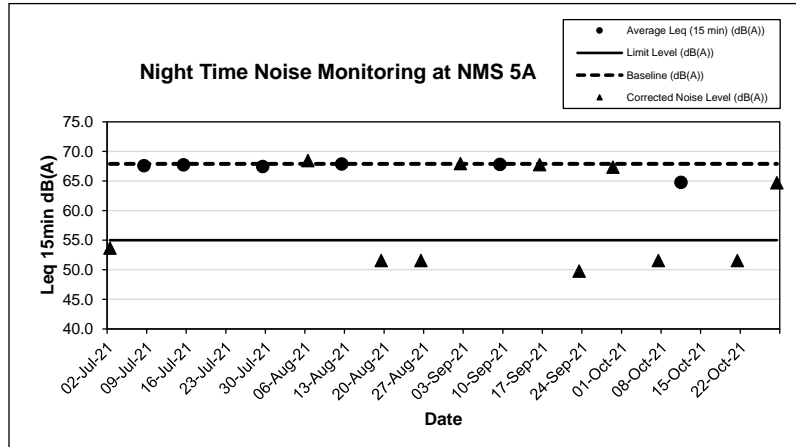

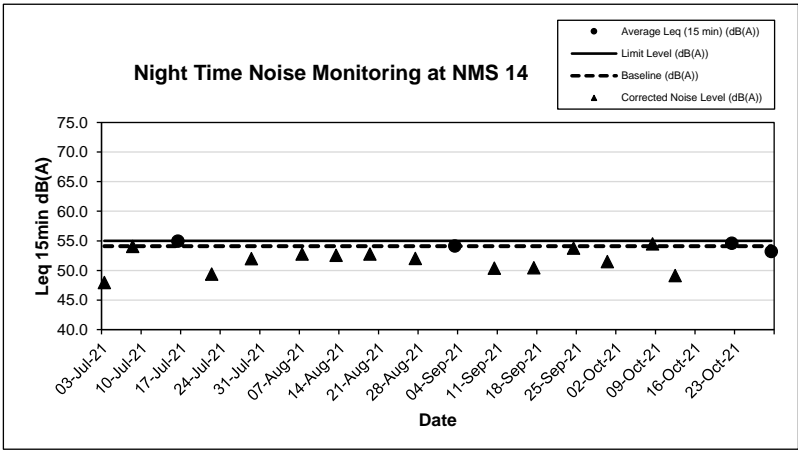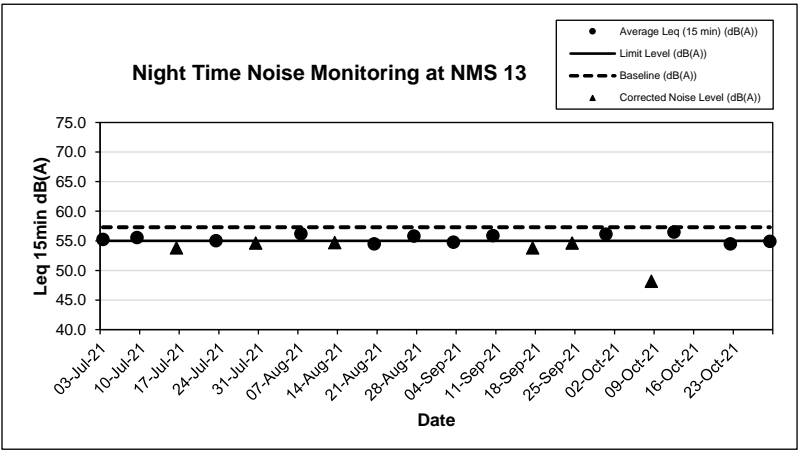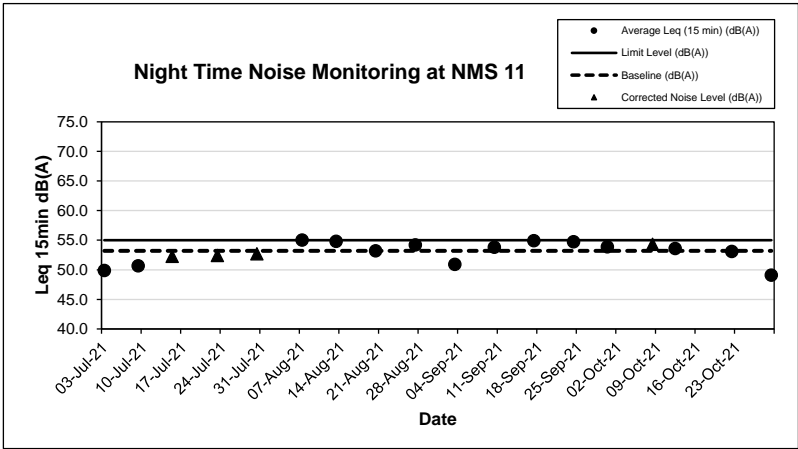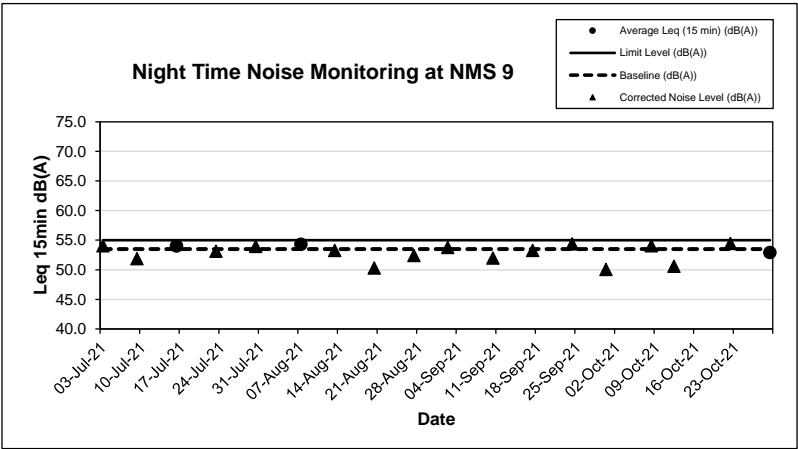

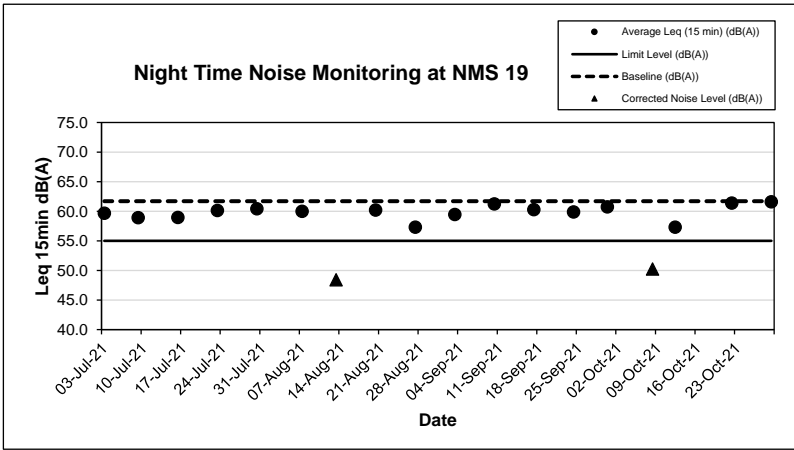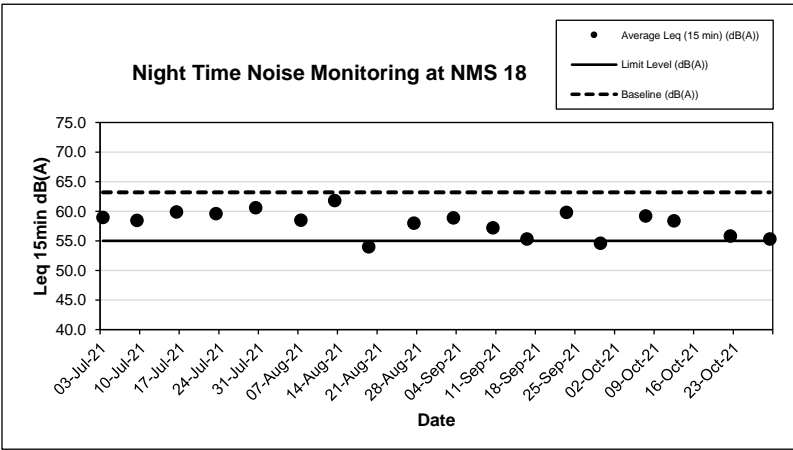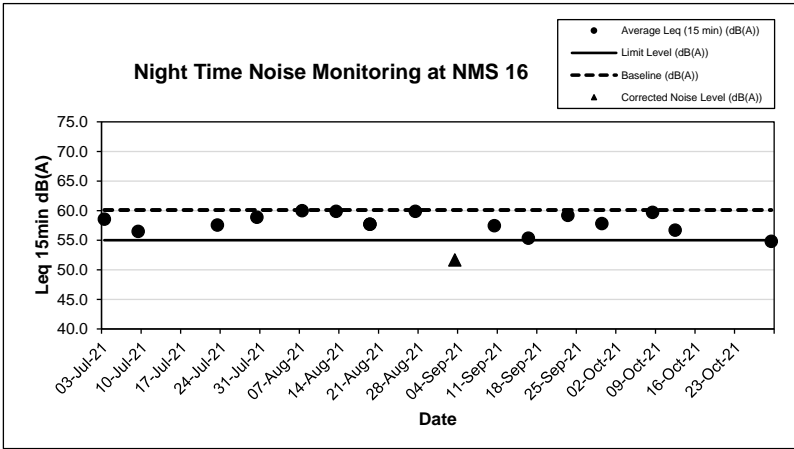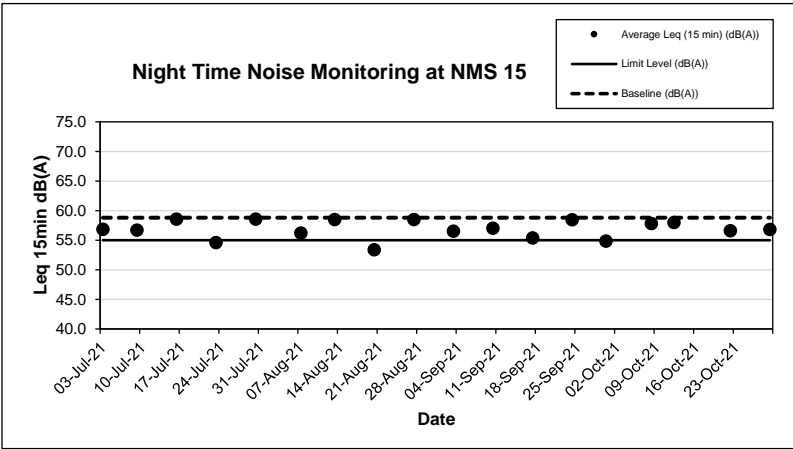

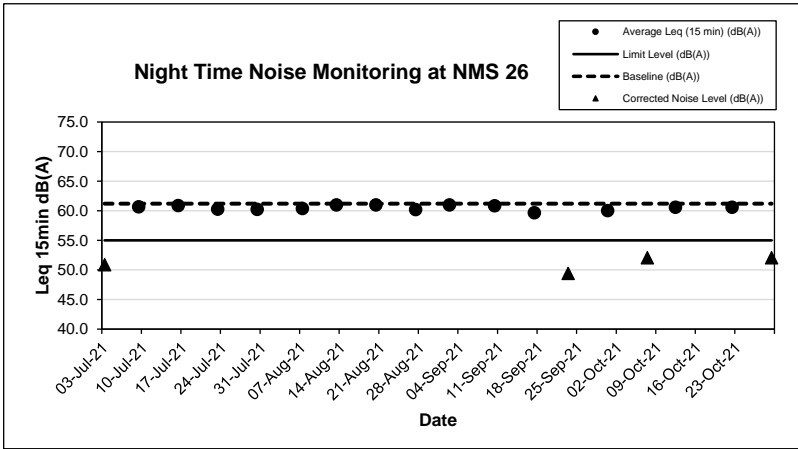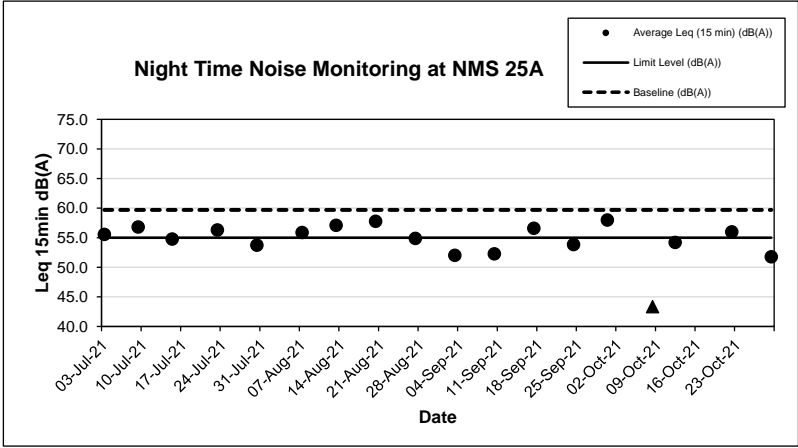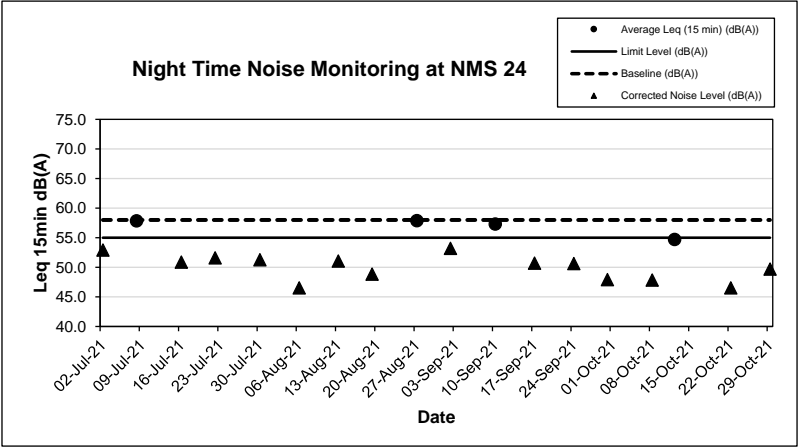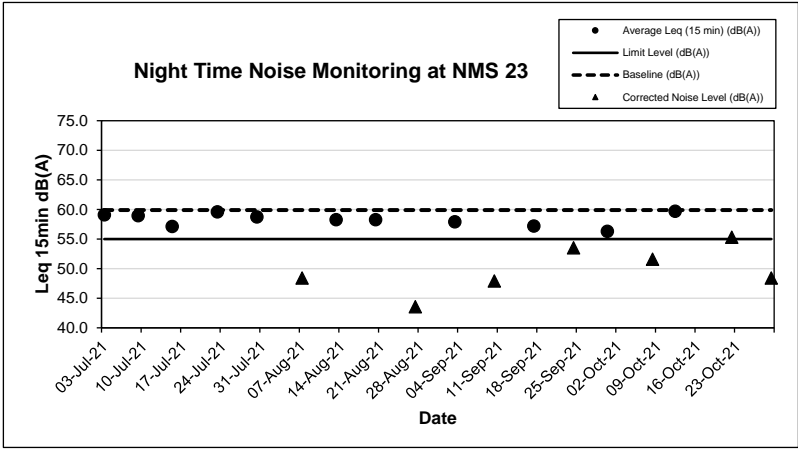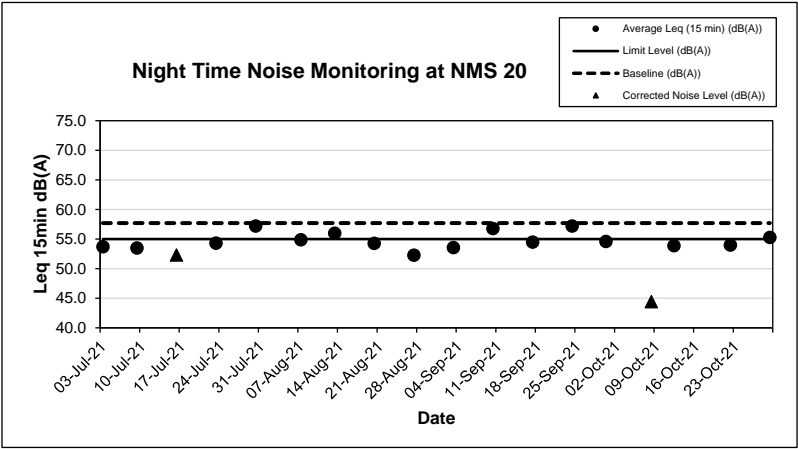

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix H

Events and Action Plan

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Event and Action Plan for Construction Dust Monitoring

EVENT	ACTION			
	ET Leader	IEC	SO	Contractor
Action Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the IEC and the SO. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET Leader. 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice. 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the IEC and the SO. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency to daily. 5. Discuss with the IEC and the Contractor on remedial actions required. 6. If exceedance continues, arrange meeting with the IEC and the SO. 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET Leader. 2. Check the Contractor's working method. 3. Discuss with the ET Leader and the Contractor on possible remedial measures. 4. Advise the SO on the effectiveness of the proposed remedial measures. 5. Supervisor implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification. 2. Implement the agreed proposals. 3. Amend proposal if appropriate.
Limit Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the SO and the EPD. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of Contractor's remedial actions and keep the IEC, the EPD and the SO informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET Leader. 2. Check Contractor's working method. 3. Discuss with the ET Leader and the Contractor on possible remedial measures. 4. Advise the SO on the effectiveness of the proposed remedial measures. 5. Supervisor implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Amend proposal if appropriate.
2. Exceedance	<ol style="list-style-type: none"> 1. Notify the IEC, the SO and the EPD and the 	<ol style="list-style-type: none"> 1. Discuss amongst the SO, ET 	<ol style="list-style-type: none"> 1. Confirm receipt of 	<ol style="list-style-type: none"> 1. Take immediate action to avoid

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EVENT	ACTION			
	ET Leader	IEC	SO	Contractor
for two or more consecutive samples	<p>Contractor.</p> <ol style="list-style-type: none"> 2. Identify the source. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. 6. Arrange meeting with the IEC and the SO to discuss the remedial actions to be taken. 7. Assess effectiveness of Contractor's remedial actions and keep the IEC, the EPD and the SO informed of the results. 8. If exceedance stops, cease additional monitoring. 	<p>Leader and the Contractor on the potential remedial actions.</p> <ol style="list-style-type: none"> 2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise the SO accordingly. 3. Supervisor implementation of remedial measures. 	<p>notification of failure in writing.</p> <ol style="list-style-type: none"> 2. Notify the Contractor. 3. In consultation with the Contractor on the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated. 	<p>further exceedance.</p> <ol style="list-style-type: none"> 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the SO until the exceedance is abated.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Event and Action Plan for Noise Impact

EVENT	ACTION			
	ET Leader	IEC	SO	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify the IEC and the Contractor. 2. Carry out investigation. 3. Report the results of investigation to the IEC. 4. Discuss with the Contractor and formulate remedial measures. 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET. 2. Review the proposed remedial measures by the Contractor and advise the SO accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC. 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Notify the IEC, the SO and the Contractor. 2. Identify the source. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency. 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented. 6. Inform the IEC, the SO and the EPD the causes & actions taken for the exceedance. 7. Assess effectiveness if the Contractor's remedial actions and keep the IEC and the SO informed of the results. 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst the SO, the ET Leader and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise the SO accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activities of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance, 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals 4. Resubmit proposals if problem still not under control 5. Stop the relevant activity of works as determined by the SO until the exceedance is abated.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Event and Action Plan for Landscape and Visual Impact

Event	Action		
	ET	SO	Contractor
Non-conformity on one occasion	<ol style="list-style-type: none"> 1. Identify Source; 2. Inform the Contractor and the SO; 3. Discuss remedial actions with the SO and the Contractor; and 4. Monitor remedial actions until rectification has been completed 	<ol style="list-style-type: none"> 1. Notify Contractor; and 2. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working methods; 2. Rectify damage and undertake any necessary replacement.
Repeated conformity Non-	<ol style="list-style-type: none"> 1. Identify Source; 2. Inform the Contractor and the SO; 3. Increase monitoring frequency; 4. Discuss remedial actions with the SO and the Contractor; 5. Monitor remedial actions until rectification has been completed; and 6. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Notify Contractor; and 2. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Amend working methods; 2. Rectify damage and undertake any necessary replacement.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix I

Waste Flow Table

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2018											
Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2018 Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sub-Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.013
2018 Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.004
2018 Dec	0.001	0.000	0.000	0.000	0.001	0.000	0.000	0.000	0.000	0.000	0.001
Total	0.001	0.000	0.000	0.000	0.001	0.000	0.000	0.000	0.000	0.000	0.018

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2019

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2019 Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.021
2019 Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.049
2019 Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.048
2019 Apr	0.100	0.000	0.000	0.000	0.100	0.000	0.000	0.000	0.000	0.000	0.089
2019 May	0.150	0.000	0.000	0.000	0.150	0.000	0.000	0.000	0.000	0.000	0.175
2019 Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.082
Sub-Total	0.250	0.000	0.000	0.000	0.250	0.000	0.000	0.000	0.000	0.000	0.464
2019 Jul	0.141	0.000	0.000	0.000	0.141	0.000	0.000	0.000	0.000	0.000	0.069
2019 Aug	0.431	0.000	0.221	0.000	0.210	0.000	0.000	0.000	0.000	0.000	0.154
2019 Sep	0.712	0.000	0.223	0.000	0.489	0.297	0.000	0.000	0.000	0.000	0.046
2019 Oct	0.663	0.000	0.306	0.000	0.357	1.085	0.001	0.027	0.009	0.000	0.027
2019 Nov	1.154	0.000	0.143	0.000	1.011	0.428	0.000	0.019	0.000	0.000	0.095
2019 Dec	0.849	0.000	0.023	0.000	0.826	0.074	0.000	0.014	0.001	0.000	0.034
Total	4.200	0.000	0.916	0.000	3.284	1.884	0.001	0.060	0.010	0.000	0.889

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2020

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2020 Jan	0.584	0.000	0.027	0.000	0.557	0.040	0.001	0.030	0.001	0.000	0.039
2020 Feb	1.072	0.000	0.042	0.000	1.030	0.000	0.001	0.026	0.003	0.000	0.013
2020 Mar	0.422	0.000	0.006	0.000	0.416	0.062	0.000	0.000	0.000	0.000	0.054
2020 Apr	0.450	0.000	0.000	0.000	0.450	0.000	0.002	0.085	0.003	0.000	0.025
2020 May	1.144	0.000	0.000	0.000	1.144	0.319	0.001	0.021	0.005	0.000	0.027
2020 Jun	3.660	0.000	0.000	0.000	3.660	0.077	0.001	0.027	0.004	0.000	0.048
Sub-Total	7.332	0.000	0.075	0.000	7.257	0.498	0.006	0.189	0.016	0.000	0.206
2020 Jul	2.008	0.000	0.014	0.000	1.994	0.000	0.002	0.047	0.006	0.000	0.067
2020 Aug	2.215	0.000	0.018	0.000	2.197	0.000	0.001	0.040	0.006	0.000	0.014
2020 Sep	4.305	0.000	0.000	0.000	4.305	0.000	0.002	0.042	0.009	0.000	0.044
2020 Oct	3.073	0.000	0.002	0.000	3.071	0.000	0.001	0.019	0.005	0.000	0.029
2020 Nov	1.670	0.000	0.000	0.000	1.670	0.000	0.001	0.030	0.006	0.000	0.036
2020 Dec	3.498	0.000	0.000	0.000	3.498	0.000	24.751	0.036	0.006	0.000	0.042
Total	24.101	0.000	0.109	0.000	23.992	0.498	24.764	0.403	0.054	0.000	0.438

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.
- 4) Updated data for previous month.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2021

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2021 Jan	3.196	0.000	0.000	0.000	3.196	0.000	0.001	0.048	0.855	0.000	0.053
2021 Feb	3.877	0.000	0.000	0.000	3.877	0.032	0.000	0.010	1.642	0.000	0.013
2021 Mar	7.348	0.000	0.000	0.000	7.348	0.000	0.001	0.215	0.004	0.000	0.050
2021 Apr	3.302	0.000	0.000	0.000	3.302	0.100	0.002	0.013	0.004	0.000	0.050
2021 May	2.315	0.000	0.150	0.000	2.165	0.024	0.001	0.008	0.005	0.000	0.106
2021 Jun	1.809	0.000	0.307	0.000	1.502	0.059	0.000	0.000	0.000	0.000	0.029
Sub-Total	21.847	0.000	0.457	0.000	21.390	0.215	0.005	0.294	2.510	0.000	0.301
2021 Jul	2.693	0.000	0.019	0.000	2.674	0.262	0.003	0.011	0.007	0.000	0.119
2021 Aug	3.088	0.000	0.000	0.000	3.088	0.095	0.002	0.007	0.011	0.000	0.071
2021 Sep	1.698	0.000	0.000	0.000	1.698	0.000	0.001	0.004	0.003	0.000	0.049
2021 Oct	1.500	0.000	0.000	0.000	1.500	0.279	0.002	0.003	0.005	0.000	0.021
2021 Nov											
2021 Dec											
Total	30.826	0.000	0.476	0.000	30.350	0.851	0.013	0.319	2.536	0.000	0.561

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.
- 4) Updated data for previous month.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix J

Environmental Mitigation Implementation Schedule (EMIS)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
<u>Noise Measures</u>				
3.10.2, 3.10.3, 3.10.14, 3.10.15 and Table 3.10	Within the boundaries of all construction sites.	• Scheduling the construction activities carefully according to the actual site work situation, avoid of concurrent activities and construction works fronting the affected schools, to minimize the total noise generated (max as 102dB (A)).	Contractor	Implemented
		• PME is recommended to operate in sub-grouping, and different sub-groups shall not be operated concurrently within any half hour period	Contractor	Implemented
		• The construction activities should be carried out in the daytime hours (0700 – 1900). Construction Noise Permit (CNP) for construction activities is required during evening or night time hours.	Contractor	Implemented
		• Construction work programme should be considered before actual construction work is undertaken, and noise mitigation measures should be implemented to minimize the potential construction noise impact. Selection and optimization of construction programmes, avoidance and reduction of parallel operation of noisy PME during noise sensitive periods.	Contractor	Implemented
		• Use of well-maintained and regularly-serviced plant during the works.	Contractor	Implemented
		• Plant operating on intermittent basis should be turned off or throttled down when not in active use.	Contractor	Implemented
		• Plant that is known to emit noise strongly in one direction should be orientated to face away from the NSRs.	Contractor	Not Applicable
		• Silencers, mufflers and enclosures for plant should be used where possible and maintained adequately throughout the works.	Contractor	Not Applicable
		• Fixed plants should be sited away from NSRs where possible.	Contractor	Not Applicable
		• Stockpiles of excavated materials and other structures such as site buildings should be used effectively to screen noise from the works.	Contractor	Not Applicable
3.10.4, 3.10.5 and Table 3.3		• The use of particular plant with equipment quieter than those specified in the GW-TM are recommended to reduce the noise levels generated by the plant.	Contractor	Implemented
		• Other type of quiet PME are allowed to use for their needs based on the actual construction conditions and programmes	Contractor	Implemented
3.10.6 to 3.10.9		• Temporary noise barriers provide noise attenuation by screening NSRs from stationary and mobile plants from direct line-of-sight in shadow zone.	Contractor	Implemented
		• The use of 3m high moveable barriers with skid footing and a small cantilevered upper portion should be adopted. The barrier material shall have a surface mass of not less than 14kg/m ² on skid footing with 25mm thick internal sound absorptive lining to achieve the maximum screening effect.	Contractor	Not Applicable
		• These temporary noise barriers should be located immediately adjacent to working area.	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		• The temporary noise barriers should be located along the working area to make sure the construction plant could be screened during all kinds of construction activities as far as practicable.	Contractor	Not Applicable
		• Noise jacket/muffler shall be used to cover the noisy part of the engine or at the engine exhaust of particular mobile plants respectively when temporary noise barriers are not practicable or noise reduction achieved is insufficient.	Contractor	Not Applicable
		• For the stationary plant bored pile oscillator, temporary noise barriers of sufficient height with skid footing and small cantilevered upper portion should be provided.	Contractor	Not Applicable
		• Barrier material of surface density of at least 14 kg/m ² is recommended in order to achieve the necessary screening effect.	Contractor	Not Applicable
3.10.10		• Full noise enclosures should cover the PME or fixed plants such as air compressor.	Contractor	Not Applicable
3.10.3		• Silencers, mufflers and enclosures for plant should be used where possible and maintained adequately throughout the works;	Contractor	Not Applicable
		• Where possible fixed plants should be sited away from NSRs; and	Contractor	Not Applicable
		• Stockpiles of excavated materials and other structures such as site buildings should be used effectively to screen noise from the works.	Contractor	Not Applicable
Air Quality Measures				
4.12.1 and 4.12.2	Within the boundaries of all construction sites.	• The Contractor shall notify any specific construction works as stated in the Air Pollution Control (Construction Dust) Regulation to the Authority before the commencement of such work. Dust mitigation measures stipulated in the Air Pollution Control (Construction Dust) Regulation should be implemented to control dust emissions from all construction work sites.	Contractor	Implemented
		• The Contractor shall undertake at all times to prevent dust nuisance as a result of his activities. Dust suppression measures such as the water spraying are necessary and should be installed to ensure that the air quality at the boundary of the site and at any sensitive receivers complies with the Hong Kong Air Quality Objectives.	Contractor	Implemented
		• The Contractor shall apply for a license or permit under the requirements of the relevant legislation (e.g. Air Pollution Control Ordinance and its subsidiary regulations) wherever applicable.	Contractor	Implemented
		• Watering of unpaved areas, access roads, construction areas and dusty stockpiles shall be undertaken at least eight times daily during dry and windy weather. Watering of the haul road shall be undertaken four to eight times daily during dry or windy weather. Water sprays may be either fixed or mobile to follow individual areas to be wetted as and when required. Application of suitable wetting agents, such as dust suppression chemicals, shall be used in addition to water, especially during the dry season (October to December). It is also suggested that watering with	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		complete coverage of active construction area eight times a day.		
		• Effective water sprays shall be used during the delivery and handling of all raw sand and aggregate, and other similar materials, wet dust is likely to be created and to dampen all stored materials during dry and windy weather.	Contractor	Implemented
4.12.1		• Stockpiles of sand, aggregate or any other dusty materials greater than 20m ³ shall be enclosed on three sides, with walls extending above the pile and 1 meter beyond the front of the pile.	Contractor	Not Applicable
		• Suitable chemical wetting agent such as dust suppression chemical shall be used on completed cuts and fills to reduce wind erosion.	Contractor	Not Applicable
		• Areas within the construction site where there is a regular movement of vehicles shall have a paved surface and be kept clear of loose surface material.	Contractor	Implemented
		• The Contractor shall restrict all motorized vehicles within the construction site, excluding those on public roads, to maximum speed of 20 km per hour and confine haulage and delivery vehicles to designated roadways inside the Site.	Contractor	Implemented
		• Construction working areas should be restricted to a minimum practicable size.	Contractor	Implemented
		• The Contractor shall ensure that no earth, rock or debris is deposited on public or private rights of way as result of his activities, including any deposits arising from the movement of plant or vehicles.	Contractor	Implemented
		• The Contractor shall provide a wheel washing facility at the exits from work areas to the satisfaction of the Engineer and to the requirements of the Commissioner of Police. Water in wheel washing facilities and sediment shall be changed and removed respectively at least once a month.	Contractor	Implemented
		• The Contractor shall submit details of the wheel washing facilities, which shall be usable prior to any earthworks excavation activity on the construction site. The Contractor shall also provide a hard-surfaced road between any washing facility and the public road.	Contractor	Implemented
		• In the event of any spoil or debris from construction works being deposited on adjacent land, or steams, or any slit being washed down to any area, then all such spoil, debris or material and silt shall be immediately removed and the affected land and areas restored to their natural state by the Contractor to the satisfaction of the Engineer.	Contractor	Partially Implemented
		• If spoil cannot be immediately transported out of the Site, stockpiles should be stored in sheltered areas.	Contractor	Implemented
• Plant and vehicles shall be inspected annually to ensure that they are operating efficiently and that exhaust emissions are not causing a nuisance. All site vehicle exhausts should be directed vertically upwards or directed away from ground.	Contractor	Implemented		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
4.12.1, 4.13.1 and Table 8.2		• Construction dust monitoring shall be carried out at representative monitoring locations during the construction period.	Contractor	Implemented
		• Path for complaints and handling procedures should be set up and implement.	Contractor	Implemented
NA		• Dark smoke emission shall be control in accordance with the Air Pollution Control (Smoke) Regulation and ETWB TCW 19/2005.	Contractor	Implemented
		• Plant and equipment should be well maintained to prevent dark smoke emission.	Contractor	Implemented
		• Only approved or exempted Non-road Mobile Machineries (NRMMs) including regulated machines and non-road vehicles with proper labels are allowed to be used in specified activities on-site.	Contractor	Partially Implemented
<u>Water Quality Measures</u>				
5.7	Within the boundaries of all construction sites.	• Silt-laden surface run-off should be prevented from directly entering the sensitive receivers during the construction works. The mitigation measures described below for the construction phase are in accordance with ProPECC PN 1/94:	Contractor	Partially Implemented
		• Construction works should be programmed so as to minimise excavation during the wet season (April to September). If this is not possible then measures should be taken to minimise the areas exposed by covering temporary exposed slopes with tarpaulins or similar material, the protection of temporary road surfaces with gravel or crushed stone and the early reinstatement of final surfaces with hydro seed grass/shrub mixture. This latter measure would have the added benefit of reducing the windblown dust during the dry season. Where temporary covering of slopes is required this should be carried out before the onset of the rainfall or storm.	Contractor	Implemented
		• Existing and newly constructed open manholes should be covered and sealed to prevent run off and water borne debris entering the drainage network without having previously passed through a sediment trap.	Contractor	Partially Implemented
		• Stock piles of construction materials, sand and gravel or excavated material should be covered with tarpaulins prior to rainstorms. The washing of material from the stockpiles directly into the storm drains should be prevented by passing the run off through a sediment trap.	Contractor	Partially Implemented
		• The surface water from the site should be discharged into storm water drain after passing through sand and silt traps designed to accommodate the maximum discharge from the site. Within the site channels, bunds or sandbags should be used to direct run off into the traps. Storm water from outwit the site should be prevented from washing over the site by the construction of interceptor channels at the site boundary. Both perimeter channels and the sedimentation traps should be constructed prior to the commencement of site formation and earthworks.	Contractor	Partially Implemented
		• The efficiency of the interceptor channels, traps and sedimentation chambers should be maintained	Contractor	Partially Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		by regular cleaning of accumulated silt and sand. Particular attention should be paid to maintenance following heavy rainfall and immediately after the issue of heavy rainfall warning by the Hong Kong Observatory.		
		• The ingress of rainwater into trenches should be minimised by the construction of bunds to prevent water flowing into the trench and covering by tarpaulins to prevent direct entry. The lengths of excavated trenches should be minimised and backfilled at the earliest opportunity. Water pumped from the trenches should be discharged to the storm water drains following passage through a suitable silt trap.	Contractor	Implemented
		• Any ground water seeping into any trenches or foundation works should be passed through a silt trap prior to discharge to the storm water drains.	Contractor	Implemented
		• The water used for the washing down of mixing drums used for onsite batching of concrete and delivery lorries for off-site batched concrete should be recycled whenever possible. Wastewater generated from the washing which is discharged should be passed through a silt trap before discharge to the storm water system.	Contractor	Not Applicable
		• The wastewater from the washing of the wheels and subframe of vehicles returning from the site onto public roads will contain suspended solids and debris. A washing bay should be provided at the exit from the site and should, where practicable, incorporate water recirculation. Water from the washing bay which is discharged to the storm water system should first be passed through a silt trap which also includes an oil/grease removal weir.	Contractor	Implemented
		• Plant maintenance areas should be paved to prevent waste oils soaking into the ground. Where possible the area should be undercover to minimise the formation of runoff and any runoff from the paved area passed through an oil trap before being discharged to the storm drains. Fuel storage tanks should be surrounded by bunds with a capacity of at least 150% of the storage capacity. The bunded areas should be able to be drained of rain water through the petrol interceptor and accumulated rain removed at regular intervals.	Contractor	Not Applicable
		• Waste oils from the site should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance and absorbent cloths and granules should be available for the cleanup of spillages.	Contractor	Implemented
		• Sewage from toilets and kitchens should be discharged directly into a foul sewer. If it is not possible to locate the site offices within easy access of a foul sewer a septic tank and soakaway should be constructed before the offices are occupied. Chemical toilets should be emptied on a daily basis and the contents taken to a foul sewer or the Sha Tin Sewage Treatment Works for disposal.	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		Wastewater collected from canteen kitchens should be discharged to the foul sewers via grease traps which provide a minimum of 20 minutes retention during peak flow. All discharges into foul sewers and storm sewers should have to be complied with TM standards under WPCO.		
		• Run off from roofed surfaces of site facilities should be collected and diverted to a storm water drain. Passage through a silt trap is only required if the water is diverted via open channels which might accumulate solids during non-rainy periods or which intercept surface run off from unpaved areas.	Contractor	Not Applicable
		• Discharges from the site shall be required to meet the terms and conditions of a valid WPCO Water Pollution Control Ordinance (WPCO).	Contractor	Implemented
Section 12.6 of the Approved EIA Report		• Regular site inspection of the construction works shall be carried out to determine compliance with the recommended mitigation measures. Inspection should be included:		
		(i) The functioning of onsite surface water collection channels and sediment traps.	Contractor	Partially Implemented
		(ii) The functioning of interception channels at the boundary of the works areas	Contractor	Partially Implemented
		(iii) The covering of stockpiles of fill and construction materials and the routing of any run off through the sediment traps.	Contractor	Partially Implemented
		(iv) The pumping procedures for emptying trenches and other excavations and the use of silt traps prior to the discharge of the water to the storm water system.	Contractor	Implemented
		(v) The use of washwater for hosing down concrete mixing and delivery vehicles and other vehicles leaving the site and the routine of excess water from the facility through sediment traps.	Contractor	Implemented
		(vi) The operation of the plant maintenance areas to control small spillages and the correct management of the fuel storage bunded area.	Contractor	Implemented
		(vii) The connection of the site office wastewater discharge to an existing foul sewer if appropriate or the operation of the kitchen wastewater grease trap and the regular emptying of the chemical toilets	Contractor	Implemented
		(viii) The operation of the roof rain water collection and drainage system.	Contractor	Implemented
<i>Landscape and Visual Mitigation Measures</i>				
Construction Phase				
Table 6.5	During construction within the Project Boundary.	• Existing trees shall be preserved as much as possible. Detailed tree preservation and transplanting proposals shall be submitted to relevant government departments for approval in accordance with DEVB TC (W) No. 7/2015.	Contractor	Implemented
		• Topsoil will be conserved as far as possible during the road improvement works and utilized during the replanting operations. The stock piling height of the topsoil will not be more than 2m.	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase	
		• Old and valuable trees (OVTs) identified in the Project Boundary shall be protected in accordance with ETWB TCW no. 29/2004.	Contractor	Implemented	
		• Night-time lighting glare shall be properly managed and control during construction so as to minimize any adverse visual impact on adjacent VSRs.	Contractor	Implemented	
		• Decorative screen hoarding with design compatible with the surrounding landscape setting shall be erected along the southern boundary of Tai Po Road to mitigate any potential adverse impact on adjacent Pedestrian and Cyclists on Footpath/Bicycle Track.	Contractor	Not Applicable	
	Operation Phase				
	During construction within the Project Boundary.	• Compensatory planting shall be provided within and outside the project boundary where possible. Detailed compensatory planting proposal will be prepared in accordance with DEVB TC (W) No. 7/2015.	Contractor	Not Applicable	
		• Planting shall be undertaken at the earliest practical time in the construction period. The planting proposal shall aim to strengthen the existing tree species and supplement the existing tree planting to provide an effective screen to ameliorate any potential landscape and visual impacts. The proposed species to be utilized for road improvement works shall be agreed with LCSD and future maintenance authorities. All the proposed species for compensatory planting shall be suitable for roadside streetscape planting.	Contractor	Not Applicable	
		• Provision of visually pleasing noise barriers and enclosures design shall be proposed. The design of these structures aims to minimize any potential visual impact and visually integrate the proposed structures into the adjacent landscape context. This should be achieved through the use of form, color, tones, materials and planting materials.	Contractor	Not Applicable	
		• Aesthetically pleasing hard landscape treatment of the carriageway and roadside furniture shall be proposed, including development of chromatic themes in the architectural treatment of engineering structures, and the consideration of landscape lighting and special landscape features.	Contractor	Not Applicable	
		• Shrubs and climbers planting are proposed on the facade of Noise Enclosures and Barriers to mitigate any adverse impact on adjacent VSRs in area where space for tree planting is not feasible.	Contractor	Not Applicable	
	Waste Management Measures				
7.6.2 to 7.6.4	Within the boundaries of all construction	• In accordance with ETWB TC (W) No. 19/2005 - Environmental Management on Construction Sites", the Contractor shall prepare and implement a Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP). The EMP shall describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different	Contractor	Implemented	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
7.6.5 to 7.6.6	sites.	categories of waste to be generated from the construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval.		
		• The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor.	Contractor	Implemented
		• Recommendations of good site practices and waste reduction measures should be stated in order to achieve avoidance and minimization of waste generation in the hierarchy.	Contractor	Implemented
		• Environmental Management Plan (EMP) and trip-ticket system shall be implemented for monitoring management of waste.	Contractor	Implemented
7.6.7	Within the boundaries of all construction sites as well as transportation routes to designed areas for off-site disposal of materials/Prior to and during construction activities.	• Specific measures targeting the mitigation of impacts in works areas and the transportation of spoil off-site should be provided to minimize the potential impacts to the surrounding environment.	Contractor	Implemented
		• To facilitate adoption of the best-practice philosophy, training shall be provided to all personnel working on site. The training shall promote the concept of general site cleanliness and clearly explain the appropriate waste management procedures defined in the EMP. Overall, the training should encourage all workers to reduce, reuse and recycle wastes.	Contractor	Implemented
7.6.8 to 7.6.9		• The contractor's environmental performance shall be monitored and controlled through the weekly environmental walks. The items after the environmental walks shall include:		
		• A review of the EMP in particular the suitability of the environmental measures on nuisance abatement and waste management adopted by the contractor;	Contractor	Implemented
		• The environmental performance of the contractor and his sub-contractors;	Contractor	Implemented
		• The effectiveness of the environmental measures on nuisance abatement and waste management implemented on the site, and any complaints received; and	Contractor	Implemented
		• The promptness of rectification or improvement actions of the Contractor on the defects and deficiencies identified during inspections of the site.	Contractor	Implemented
		• Waste shall only be disposed of at licensed sites and the WMP should include procedures to ensure that illegal disposal of wastes does not occur. Only waste haulers authorized to collect the specific category of waste concerned should be employed and a trip ticket system shall be implemented for offsite disposal of inert C&D materials and non-inert C&D materials at public fill reception facilities and landfills, respectively. Appropriate measures should be employed to minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		enclosed containers.		
7.6.10		<ul style="list-style-type: none"> Work site(s) shall be arranged and managed to facilitate the proper management of wastes and materials. The WMP shall include plans indicating specific areas designated for the storage of particular types of waste, reusable and recyclable materials as well as areas and management proposals for any stockpiling areas. Waste storage areas should be well maintained and cleaned regularly. Specific provisions for different types of material are outlined below. In general, these areas should be designed to avoid cross contamination of materials as well as pollution of the surrounding environment. 	Contractor	Implemented
7.6.11 to 7.6.14		<ul style="list-style-type: none"> In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the excavated fill materials should be reused on site as backfill material as far as possible. 	Contractor	Implemented
		<ul style="list-style-type: none"> Careful design, planning and good site management should be maintained in order to minimise over ordering and generation of surplus materials such as concrete, mortars and cement grouts. The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse. 	Contractor	Implemented
		<ul style="list-style-type: none"> C&D materials should be segregated on site into different waste and material types. The Contractor should clearly demonstrate in the EMP how he intends to maximise the reuse of C&D material on-site. Where reuse of materials on site is not feasible, the Contractor should explore opportunities for recycling materials off-site, and inert C&D materials shall be reused on site as much as possible. 	Contractor	Implemented
		<ul style="list-style-type: none"> Paving bricks arising from existing pavement should be recycled on site as much as possible. 	Contractor	Not Applicable
		<ul style="list-style-type: none"> Existing marginal roadside barriers comprise pre-cast units should be reused in the following widening works as much as possible, 	Contractor	Not Applicable
		<ul style="list-style-type: none"> Existing bridge parapets comprise aluminum post and railings, which have a recyclable value and should be sold for reconditioning or reused for scrap metal as much as possible 	Contractor	Not Applicable
		<ul style="list-style-type: none"> Any stockpile should be sited away from existing watercourses and suitably covered to prevent wind erosion and impacts on air and water quality. 	Contractor	Not Applicable
7.6.15 to 7.6.17		<ul style="list-style-type: none"> Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows. Containers used for the storage of chemical wastes should: <ul style="list-style-type: none"> be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; 	Contractor	Partially Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		• have a capacity of less than 450L unless the specifications have been approved by the EPD; and	Contractor	Implemented
		• display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation (Cap. 354C).	Contractor	Implemented
		The storage area for chemical wastes should:		
		• be clearly labelled and used solely for the storage of chemical waste;	Contractor	Implemented
		• be enclosed on at least 3 sides;	Contractor	Partially Implemented
		• have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;	Contractor	Partially Implemented
		• have adequate ventilation;	Contractor	Implemented
		• be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and	Contractor	Partially Implemented
		• be arranged so that incompatible materials are adequately separated.	Contractor	Implemented
		The Contractor shall register with EPD as a Chemical Waste Producer. Waste oils and other chemical wastes as defined in the Waste Disposal (Chemical Waste) (General) Regulation will require disposal by appropriate means and could require pre-notification to EPD prior to disposal. Appropriate means include disposal:		
		• via a licensed waste collector; and	Contractor	Implemented
		• to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers; or	Contractor	Implemented
		• to a reuser of the waste, under approval from EPD.	Contractor	Not Applicable
7.6.18 to 7.6.20		• General refuse generated on-site should be stored in enclosed bins or compaction units separate from construction and chemical wastes. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily or every second day basis to minimize odour, pest and litter impacts. The burning of refuse on construction sites is prohibited by law.	Contractor	Partially Implemented
		• Separate labelled bins should be provided if feasible.	Contractor	Implemented
		• Office waste can be reduced through recycling of paper if volume is large enough to warrant collection. Participation in a local collection scheme should be considered if one is available.	Contractor	Implemented
7.7.1		• All wastes produced during the construction of the Project shall be handled, stored, and disposed of in accordance with good waste management practices and relevant regulations and	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		requirements.		
		<ul style="list-style-type: none"> The mitigation measures recommended in the EIA/EIA review report should form a basis of the WMP to be developed by the Contractor in the construction phase of the Project. 	Contractor	Implemented
EP 1.5	<u>General Condition</u>			
N.A	During construction within the Project Boundary.	<ul style="list-style-type: none"> The Permit Holder shall display conspicuously a copy of this Permit on the Project site(s) at all vehicular site entrance/exits or at a convenient location for public information at all times. The Permit Holder shall ensure that the most updated information about the Permit, including any amended Permit, is displayed at such locations. If the Permit Holder surrenders a part or the whole of the Permit, the notice he sends to the Director shall also be displayed at the same locations as the original Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site(s). 	Contractor	Partially Implemented

Implementation status: Implemented / Partially Implemented / Not Implemented / Not Observed / Not Applicable

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix K

Weather and Meteorological Conditions during Reporting Month

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Date	Mean Pressure (hPa)	Air Temperature			Mean Relative Humidity (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)		
October 2021						
1	1009.1	33.1	30.3	28.8	79	Trace
2	1011.0	32.9	30.0	28.3	74	-
3	1012.4	29.9	28.8	27.0	79	1.9
4	1012.5	32.7	29.8	28.1	71	-
5	1011.4	32.8	30.1	28.7	69	Trace
6	1008.5	31.7	29.5	27.6	69	Trace
7	1005.7	30.8	28.8	25.0	75	43.9
8	1004.6	26.8	25.5	24.7	94	329.7
9	1004.9	27.9	26.5	25.3	91	130.3
10	1008.0	27.9	26.8	25.3	86	45.1
11	1005.4	32.7	28.5	26.0	68	-
12	1001.3	26.4	25.1	23.6	65	0.2
13	1002.5	27.4	25.8	22.9	89	57.7
14	1009.2	30.0	27.8	26.1	86	13.3
15	1010.4	27.6	26.2	25.2	85	4.6
16	1013.8	30.3	26.8	24.3	73	Trace
17	1018.0	28.0	24.2	22.2	68	-
18	1018.3	27.7	23.9	20.9	70	-
19	1017.8	28.9	25.7	23.5	75	-
20	1015.9	29.8	26.8	25.0	78	0.1
21	1014.9	28.2	24.2	19.3	80	0.7
22	1019.2	20.5	19.3	18.2	77	Trace
23	1020.1	22.7	20.5	18.3	75	-
24	1018.9	26.6	22.1	19.8	69	-
25	1016.6	27.5	23.1	19.7	66	-
26	1015.8	28.3	25.1	22.7	69	-
27	1016.7	27.0	25.6	24.9	76	Trace
28	1017.9	28.0	25.7	24.2	77	0.1
29	1018.2	27.7	25.5	23.9	76	1.1
30	1009.1	33.1	30.3	28.8	79	Trace
31	1018.8	26.2	24.4	23.0	81	2.4

Source: Hong Kong Observatory

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix L

Cumulative statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Environmental Complaints Log

Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
COM-2019-005	2/2/2019	EPD	CCZJV	Noise	13/2/2019	According to the photo taken from the complainant, the complaint was related to the project. Although the tree felling works were covered by the valid CNP (GW-RN0783-18), Contractor was reminded to strictly follow and fully comply with the CNP conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. Contractor was recommended to increase the frequency of using the electrical chain saw instead of the diesel chain saw for reducing the noise impact. Environmental Team conducted additional ad-hoc noise monitoring on 19:00 14 th February 2019 to 07:00 15 th February 2019 for evaluate the effectiveness on the proposed mitigation measures. No project-related noise exceedance case on 14-15 Feb 2019 Contractor's night tree-felling and removal works. The proposed mitigation measures were effective for noise impact.	20/2/2019
COM-2019-006	22/2/2019	Project Hotline of NE/2017/05	CCZJV	Noise	26/2/2019	According to the location of complainant from Kwai Wo House, the complaint was related to the project. Although the tree felling works were covered by the valid CNP (GW-RN0783-18), Contractor was reminded to strictly follow and fully comply with the CNP conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. An extended barrier at the top acts as a cantilever shape was recommended to	4/3/2019

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						modify the existing semi-enclosure installed in the cherry picker Also, three sides with top as a semi-enclosure to be used and those tree felling activities should be inside the semi-enclosure in the ground slope. The main contractor had been recommended to review their works program and methods of tree felling as to minimize the night time tree felling activities.	
COM-2019-0010	28/3/2019	Project Hotline of NE/2017/05	CCZJV	Noise	28/3/2019	The complaint case should be related to the MTR night time maintenance works. Main Contractor used portable phones and head-set only for communication, and none of loudspeakers were allowed to be used. Main Contractor handled of tree debris into the lorry skip in care when loading. Besides, a layer of soft material (soil/tree debris) was observed leaving inside the skip of the grab lorry to reduce the loading noise. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0132-19) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour.	4/4/2019
COM-2019-0033	26/7/2019	Police visit on-site	CCZJV	Noise	26/7/2019	The complaint is related to the project. The Main Contractor comply with CNP No.: GW-RN0443-19 allowable construction site and within the site boundary to carry out night work on tree felling and the clearance of felled tree debris during the restricted hour. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0443-19) conditions and the mitigation measures stipulated in the EM&A Manual when	30/7/2019

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						construction activities are operating during restricted hour. Contractor was recommended to increase the frequency of using the electrical chain saw instead of the diesel chain saw for reducing the noise impact. Contractor was reminded to reschedule of tree felling arrangement that most of the fell branches and trunks were temporary laid on slope and arranged to cut smaller on Day Time to minimize the noise nuisance to the nearby NSRs.	
COM-2019-0045	30/8/2019	1823	CCZJV	Noise	30/8/2019	The complaint is related to the project. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0443-19) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. Contractor should strictly follow the use of acoustic enclosure as in condition 3.d.5. of the CNP during the operation of breaker, hand-held, mass $\leq 10\text{kg}$ (CNP023) shall only be operated inside the acoustic enclosure composed of four side-panels and one top-panel, so that no part of such equipment is visible from any nearby noise sensitive receiver. The panels shall be made of minimum 10mm thick plywood or 1mm thick steel outer skin and minimum 50mm thick sound absorbing lining, or equivalent construction. Contractor was reminded to use portable phones and head-set only for communication, and none of loudspeakers is allowed for night work activities.	19/9/2019

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
COM-2019-0056	9/10/2019	Project Hotline of NE/2017/05 and EPD	CCZJV	Noise	19/10/2019	The complaint of the construction noise especially the breaker noise is project related. Due to the concern of road safety, the Contractor conducted the emergency road repair works under an Emergency Excavation Permit (EXP) of Plan ID: EO13123 issued by Highways Department (HyD). The main contractor's PR / hotline staff was reminded to enhance communication with sufficient information provided for replying any enquiry / complaint in the future. The main contractor was also reminded that noise mitigation measures should be provided as far as practicable subject to the emergency situation. For construction works covered by the CNP issued by EPD, the main contractor should fully complied with the conditions as stipulated and provided all noise mitigation measures as required under the conditions of the CNP. For works subject to the emergency situation, noise mitigation measures such as noise barrier, enclosure etc. should be provided as far as practicable to minimise the noise nuisance to the NSRs.	4/11/2019
COM-2019-0057	9/10/2019	EPD	CCZJV	Noise	18/10/2019	The complaint of the generator noise nuisance is related to the project. The concerned portable generator is supplying electric power for the Variable Message Sign (VMS) showing the speed limit in 50 km/hr. It is switched on and off manually by manpower, and would only be operated between daytime 07:00-19:00. No construction noise permit (CNP) should be	21/10/2019

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						required as the portable generator is not operating in restricted hours. The main contractor was reminded to strictly follow the use of their proposed semi-enclosure as the mitigation measures for the portable generator and the generator operates in daytime 07:00-19:00 only.	
COM-2019-0066	6/11/2019	EPD	CCZJV	Noise	7/11/2019	The complaint of the emergency road repair work is related to the project. The works on on 5 th November 2019 between 22:00 and 06:00 the next day at southbound slow lane of Tai Po Road outside Wai Wah Centre, including breaking operation. The main contractor should inform the EPD in advance of any emergency opening works of the Project in future to facilitate the effective handling of noise complaint that may arise.	12/11/2019
COM-2020-0083	29/02/2020	Project email of NE/2017/05	CCZJV	Noise and Dust	29/02/2020	The complaint of the dust and noise nuisance near Wai Wah Centre during both the day and night works was at zone 2. The construction works at zone 2 was the mini-piling operation during the day time was same as the complaint. Thus, the complaint in daytime is related to the project. Furthermore, loading and unloading works was carried in night time. Contractor was reminded to enhance the water spray frequency on the construction site for mitigation measures on dust control. Also, Contractor should provide green tarpaulin curtain and additional acoustic Sound Proof Canvas as a secondary layer at the bottom of the mini-pile drilling machine to secure the total enclose condition to minimize the visual and noise impacts	19/03/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>to nearby NSRs.</p> <p>ET checked the regular impact air and noise monitoring data between day time and night-time regular noise monitoring data, no exceedance case was found on both regular impact air and noise monitoring measurement.</p> <p>The main contractor should carry out further review the effectiveness of the enclosure or noise barrier with their mitigation measure and propose alternative noise mitigation measures to enhance the noise reduction on similar day works or night works in restricted hours.</p>	
COM-2020-0089	24/03/2020	Project hotline	CCZJV	Noise	24/03/2020	<p>A resident of Wai Wah Centre complained that noise generated from construction activities at night disturbing the nearby resident. According to the Contractor's information, loading/unloading, steel bar cutting, steel plate grinding and asphalt compaction were carried out in the early hours of 24th Mar 2020. The night work activities were within the site boundary. Also, 4 sides with top cover acoustic enclosure for the portable generator was used during the night work. Furthermore, mitigation measures listed in the CNP were implemented for PME and works activities. Three sides with top cover enclosure and additional acoustic comprised with 50 mm sound absorbing lining were used for night works activities. ET analysed that the complaint noise source should not be project-related construction noise.</p>	07/04/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
COM-2020-0090	27/03/2020	Project hotline	CCZJV	Noise	27/03/2020	Both complaint cases were concerning about the noise nuisance generated from the construction work activities at night time disturbing the nearby Wai Wah Centre residence. According to the Main Contractor, similar nature of major construction works carried out between 03:00 a.m. and 04:00 a.m. on 27 th & 28 th March 2020 was the asphalt compaction for the road surface remedial works at zone 2 south lane adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0002-20 that is within the allowable construction site location and within the site boundary to carry out night work on loading and unloading works. ET conduct regular night-time noise monitoring at all monitoring stations between 23:00 26 th March 2020 to 04:00 27 th March 2020, and between 23:00 2 nd April 2020 to 04:00 3 rd April respectively. No exceedance cases were found on both ET regular night-time noise monitoring measurement. ET did not remark on-site any noise related to construction works at above noise monitoring nights for which the results were lower than baseline noise level. Hence, ET analysed that the dominant noise source should be road traffic noise but not the project-related construction noise.	04/05/2020
COM-2020-0091	28/03/2020	Project hotline	CCZJV	Noise	28/03/2020		
COM-2020-0093	06/04/2020	Project hotline	CCZJV	Noise	06/04/2020	The complaint case on 6 th Apr was received by project hotline. The major construction works between (10:00pm – 11:00pm) on 6 th April 2020 was TTA implementation works and asphalt removal works for the road surface remedial work	28/04/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						at zone 2 adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0152-20 that is within the allowable construction site location and within the site boundary to carry out night work on loading and unloading works. The five noise monitoring stations close to the concerned works area are NMS3, NMS4, NMS5A, NMS6A & NMS7, and NMS5A & NMS6A locate nearest to Wai Wah Centre. The night time noise monitoring results measured at NMS3, 4 & 6A were all lower than that of measured in the baseline, two exceedance case were found at NMS 5A especially NMS 5A & NMS 6A monitoring stations where locate at the Wai Wah Centre. The corrected noise level measured at NMS 7 is lower than the night time limit 55dB (A). Therefore, there was no exceedance cases were found on ET regular night-time noise monitoring measurement. ET analyzed that the dominant noise source should be road traffic noise but not the project-related construction noise.	
COM-2020-0096	20/04/2020	Project hotline	CCZJV	Noise	20/04/2020	A continues complaint were received on 20 Apr and 21 Apr 2020. A resident of Wai Wah Centre filed three complaints about the noise nuisance generated by the nearby construction activities during daytime. Two complaints were made through project hotline on 20 th Apr 2020 at 10:57 a.m. and 21 st Apr 2020 at 9:03 a.m., while the other one was through project email on 20 th Apr 2020 at 12:43 p.m. The noise source(s) of the concerned nuisance during complaint period	19/05/2020
COM-2020-0097	20/04/2020	Project Email	CCZJV	Noise	20/04/2020		
COM-2020-0098	21/04/2020	Project hotline	CCZJV	Noise	21/04/2020		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>should be mini piling works, which is opposite to Wai Wah Centre. According to the contractor's work schedule, major day work activity was mini-piling operation since early Feb 2020 at zone 2 in central median at non-restricted hours, from Mondays to Saturdays between 0800 and 1800 not including General Holidays. The mini piling operation on 20th & 21st Apr 2020 was carried out at non restricted hours. The limited level of noise generated by the construction of the Project during the non-restricted daytime hours will be 75 dB (A) for dwelling. The mini piling operation on 20th and 21st Apr 2020 was carried out at non restricted hours with green tarpaulin curtain and sound proof canvas. The noise level of NMS 5A and NMS 6A on 22nd Apr 2020 were 73.5 dB (A) and 72.6 dB (A) respectively. No noise exceedance was occurred at NMS 5A and NMS 6A. The construction activity on 22nd Apr 2020 was similar to 20th and 21st Apr 2020. Therefore, ET's day-time monitoring result on 22nd April 2020 at NMS5A and NMS6A can act as a reference for impact noise from the similar mini-piling operation on 20th and 21st April 2020. ET analyzed that the dominant noise source should be road traffic noise but not the project-related construction noise.</p>	
COM-2020-0099	21/04/2020	Project hotline	CCZJV	Noise	21/04/2020	<p>The complaint cases on 21st Apr 2020 was received by project hotline from Police. According to the complainant who is the local resident at Wai Wah Centre, the noise source(s) of the concerned</p>	05/05/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						nuisance during night works was at zone 2 is opposite to Wai Wah Centre. The major construction works was road surface remedial work since 15 th April 2020 conducted at restricted hours along zone 2 south boundary adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0152-20 that is within the allowable construction site location and within the site boundary to carry out night work on road surface remedial works. Environmental Team (ET) conduct a regular night-time noise monitoring at all monitoring stations between 23:00 23 rd April 2020 to 04:00 24 th April 2020. The five noise monitoring stations close to the concerned works area are NMS3, NMS4, NMS5A, NMS6A & NMS7, and NMS5A & NMS6A locate nearest to Wai Wah Centre. There were no exceedance on the night time noise monitoring, especially measured at NMS 5A & NMS 6A where locate at the Wai Wah Centre, the measured result at NMS 5A & 6A were all lower than that of measured in the baseline. Therefore, no exceedance cases were found on ET regular night-time noise monitoring measurement. ET analyzed that the dominant noise source should be road traffic noise but not the project-related construction noise.	
COM-2020-0100	23/04/2020	Project hotline	CCZJV	Noise	23/04/2020	The complaint was received via project hotline on 23 rd April 2020 at 10:45 a.m. A resident of Wai Wah Centre complained that noise generated from operation of the two piling machines	11/05/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>disturbing her daughter's study for DSE examination, and demanding limitation on operation hours of the machines only at two separate periods between 12 noon and 1p.m and 3 p.m. to 6 p.m. According to the Main Contractor, the major construction works at day time (08:00-18:00) on 23rd April 2020 was mini-piling operation at Zone 2 Central Median of Tai Po Road near Wai Wah Centre. According to the photo records of day-time site condition on 23rd April 2020 provided by Main Contractor, the green tarpaulin curtain was provided for the mini-pile drilling machines so that the bottom part of the mini-pile drilling machine was blocked from view of nearby NSR (e.g. residents at Wai Wah Centre) and an additional layer of sound proof canvas was installed at lower level to mitigate the noise from mini-pile drilling operation. The day-time noise monitoring results measured at NMS3, 4, 5A, 6A and 7 were all lower than the limit level, especially NMS 5A & NMS 6A monitoring stations where locate at the Wai Wah Centre. The monitoring results show no noise exceedance occurred at both locations. Thus, ET day-time monitoring result on 22nd April 2020 at NMS5 & NMS6 can be act as a reference for impact noise from the similar mini-piling operation activities on 23rd April 2020. Therefore, there was no exceedance cases were found in ET regular day-time noise monitoring measurement. ET analyzed that the dominant noise source should be road</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						traffic noise but not the project-related construction noise.	
COM-2020-0101	28/04/2020	1823	CCZJV	Noise	28/04/2020	The complainant on via ICC1823 on 28 th April 2020 complained about the noise and odor nuisance generated from the night-time asphalt laying construction works at Shatin Rural Committee Road (Zone 3) area. Although the main contractor no work at zone 3, but the major night-time construction works was road surface remedial work which was related to the complainant concerned. The major construction works was road surface remedial work since 15 th April 2020 at approved restricted hours along zone 2 south boundary adjacent to Wai Wah Centre. Also, Tai Po Road is the main strategic route, implementation of temporary traffic diversion at day time due to loading and unloading material or plant work or road surface remedial work is not feasible. The lorry had been used in TTA implementation & road opening, portable generator and electric handheld breaker had been used in asphalt removal work, dump truck with grab had been used for loading and unloading of asphalt or rubble, vibratory compactor had been used in asphalt compaction for road surface remedial works on 27 th & 28 th April 2020. The Main Contractor complied with CNP No.: GW-RN0152-20 that allowed PME used in Group C or Group F. According to the Main Contractor, advance "Notice to Affected Residents" had been issued and distributed on	15/05/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						26 th March 2020 in accordance with the CNP advice that prior notification should be given to nearby residents. Besides, the road re-surfacing work would be carried out at approximately 14 night-time works between 2 nd and 28 th April 2020 listed in the distributed notices. No exceedance cases were found on ET regular night-time noise monitoring measurement at all noise monitoring stations, especially measured at NMS 5A & NMS 6A where locate close to the works area (Wai Wah Centre in Zone 2), the measured result at NMS 5A & 6A were all lower than that of measured in the baseline. ET analyzed that the dominant noise source should be road traffic noise but not the project-related construction noise.	
COM-2020-0151	10/11/2020	EPD	CCZJV	Water	10/11/2020	The complainant on 10 th November 2020 complained about water discharge onto the traffic lanes of Northbound towards Sha Tin Section of Tai Po Highway. According to the Main Contractor, there is one active site access located at Zone 1 (R1) near Pai Tau, site access no. is N02. Restricted opening hours of the site access Zone 1 (R1) is between 10:00 to 16:00. The operation which might be related to the complaint was water flow from water-filled barriers before the opening of site access and no water spilling onto the traffic lanes from the access area of Zone 1 (R1). The released water was directed towards to the work areas facing Zone 1 (R1) and no water was flowed towards the high-speed road	27/11/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						or traffic lanes. ET conducted ad-hoc site inspection on 17 th November 2020. ET had no particular findings related to the complaint and conducted trial to open the bottom of the water barrier valve for testing and checking on the water flow to the construction site at Zone 1. Contractor performed well on environmental preventive measures for soil or silt leakage protection as impervious sheet with sand bags had been provided at the site boundary of Zone 3. ET analyzed that released water was directed towards to the work areas facing Zone 1 (R1) and no water was flowed towards the high-speed road or traffic lanes.	
COM-2020-0152	20/11/2020	1823	CCZJV	Noise	20/11/2020	The complainant on via ICC1823 on 20 th November 2020 complained about the noise generated from the night-time asphalt laying construction works between Sha Tin Station and nearby Wo Che Estate. Although the main contractor no work at zone 5, but the major night-time construction works was road surface remedial work which was related to the complainant concerned. According to the Main Contractor, the major construction works was road surface remedial work since 19 th November 2020 conducted at restricted hours along zone 3 to zone 4 north bound of Tai Po Road Sha Tin section. 3.20 No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix F) at all noise monitoring stations. Contractor placed acoustic enclosure	7/12/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>“SilentCUBE” with four sides and a top cover at asphalt removal works to mitigate. The Main Contractor was reminded to pay attention to CNP other condition 3.d.3, the electric hand-held breaker shall only be used for carrying out construction work between 22:00 – 23:30 hours. It is prohibited to use the electric hand-held breaker beyond the CNP condition 3.d.3 stated that the using limitation on 23:30. The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during 00:00 to 06:00 sleeping time.</p>	
COM-2020-153	26/11/2020	EPD	CCZJV	Water	24/11/2020	<p>According to EPD Mr. Bryan Kwok, EPD carried out a site inspection on 24 November 2020, revealing that muddy effluent was discharged from an outfall at Fo Tan near Jockey Club Ti-I College while construction work of the abovementioned project site at Zone 5 opposite to Wo Che Estate was in progress. EPD team inspected the condition of waste water treatment facilities on site (slope F133) and observed that the water in the first and second sedimentation tanks was muddy; muddy water was observed at the outlet level of the WetSep (waste water treatment plant) though there was no discharge and piling works at the time. EPD team reminded the Main Contractor that effluent does not comply with the discharge license standard should NOT be allowed to discharge. The waste</p>	23/12/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						water treatment system should be improved and maintained to ensure the effluent discharge standard. EPD team requested in both works area of Slope F133 and Slope F163 the Main Contractor to locate the network of drainage, connecting manhole(s) and downstream manhole, check if any presence of muddy materials and clear-out. The main contractor was reminded to strictly follow and fully comply with the water discharge license (WT00032446-2018) conditions and the mitigation measures stipulated in the EM&A Manual for effluent discharge on the wastewater treatment system.	
COM-2020154	27/11/2020	1823	CCZJV	Noise	30/11/2020	The complaint was received via ICC1823 on 27 th November 2020, the complainant expressed concern of construction noise nuisances near Wo Che Estate at around 01:14 am on 27 th November 2020. According to the Main Contractor, there were no construction works near Wo Che Estate (Zone 5) on 26 th and 27 th November 2020. The major construction works were works related to removal of central median (at night-time) under the approved road closure with CNP no.GW-RN0799-20. According to Main Contractor EO Kimberly, she sent prior notification to the EPD on 20 th November 2020 through logging in the webpage of EPD before the commencement of the construction work in relation to the CNP GW-RN0799-20 (conditions 3.d.11 and 4.d.8). The Main Contractor provided photo records showing that mitigation measures of the movable acoustic	14/12/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						enclosure "SilentCUBE" with four sides and a top cover were implemented for night work on removal of existing central median: drill hole with percussive drill for temporary steel module spiral installation, drill hole at existing central median with concrete corer and asphalt compaction with portable roller. Main Contractor was reminded to strictly follow and fully comply with the CNP No.: GW-RN0799-20 conditions. 5.11 The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during 00:00 to 06:00 sleeping time.	
COM-2020155	26/11/2020	1823	CCZJV	Dust	30/11/2020	According to the complainant, the dust nuisance concerned at day time was at the slip road to Fo Tan Road near Lok King Street near Zone 5 works area. According to the Main Contractor, the major day time construction works at Zone 5 works area in November were mini-piling works and slope works of soil replacement. Regular movement of vehicle for transportation was also carried out on site. Thus, the complaint was considered to be related to the project. ET conducted regular day-time air quality monitoring in November 2020 and on the 3 rd December 2020 at selected air monitoring stations AMS6, 8, 11A & 13 and AMS5, 4A, 7A & 12 respectively. The two air quality monitoring stations closed to the works area at zone 5 (where the complainant concerned of dust nuisance) were AMS12 and	5/1/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						AM13; and AMS13 locate nearest to Zone 5. The ET regular air quality results measured at AMS13 and AM12 in November 2020 and on the 3 rd December 2020 show that there was no exceedance case found in air quality monitoring measurement and the results were all below the action level. The Main Contractor was reminded to enhance the mitigation measures in dust control such as increase the water spray frequency at the construction site to suppress dust emission. The Main Contractor proposed to properly maintain the coverings on exposed slopes and keep them in good condition for minimizing dust impact. The Main Contractor proposed to frequently spraying of haul road especially at area where active movement of vehicles and pave the haul road where necessary to reduce dust impact.	
COM-2020157	7/12/2020	STDC	CCZJV	Dust	7/12/2020	According to the complainant, the dust nuisance concerned at day time was generated from the construction works area of the Tai Po Road Widening project at Zone 5. According to the Main Contractor, major day time construction works of mini-piling and soil replacement at slopes were carried out at Zone 5 works area in December 2020. There was also regular movement of vehicle for transportation within the works area. Thus, the complaint was considered to be related to the project. ET conducted regular day-time air quality monitoring (Appendix C) on the 3 rd , 9 th & 15 th December 2020 respectively which was close	29/12/2020

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						to the date of complaint, at selected air monitoring stations AMS5, AMS4A, AMS7A & AMS12. ET regular day-time air quality monitoring measurement results at air quality monitoring stations AMS12, closest to Zone 5. The ET regular air quality results measured at AM12 on 3 rd , 9 th & 15 th December 2020 show that there was no exceedance case was found in air quality monitoring measurement and the results were all below the action level. The Main Contractor was reminded to reduce the travelling speed of transportation vehicles on site and plan the schedule of delivery transport in order to reduce dust impact. The Main Contractor proposed to continue in maintaining the coverings on exposed slopes in good condition for minimizing dust impact. The Main Contractor proposed to increase water spraying at area where active movements of vehicle transportation occur.	
COM-2020161	18/12/2020	EPD	CCZJV	Noise	18/12/2020	The complaint was received via email notification by EPD on 18 th December 2020, the complainant expressed concern of construction noise nuisances near Wo Che Estate during night-time on 7 th & 8 th December 2020. According to the Main Contractor, the major construction works was removal of central median works since 7 th & 8 th December 2020 conducted at restricted hours along Zone 4 central median of Tai Po Road Sha Tin section. Thus, the complaint is considered to be related to the project. 3.4 According to the Main Contractor, portable generator with hand-	5/1/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						held breaker had been used for breaking of asphalt (on existing central median edge); lorry with crane, portable generator and concrete corer had been used for remove (lifting) the existing central median and coring of central median joint; dump truck with grab had been used for loading and unloading of rubble; portable roller had been used in asphalt compaction; lorry with crane, percussive and hand-held drill and portable generator had been used for installation of temporary steel module between 00:30 to 04:30 am on 7 th December 2020. The Main Contractor complied with CNP No.: GW-RN0799-20 that allowed the usage of PMEs. The noise emanated from the concrete corer for drilling hole at existing central median and portable roller for asphalt compaction might cause a noise nuisance. To further alleviate the noise nuisance, the Contractor placed acoustic enclosure "SilentCUBE" with four sides and a top cover at removal of existing central median and asphalt compaction works to mitigate as shown in the site condition photo record. No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix F) at all noise monitoring stations, especially measured at six noise monitoring stations mentioned in above section 3.15 where locate close to the works area (Sha Tin station to nearby Fung Wo Estate in Zone 4), the measured result at NMS16, NMS18 and NMS26 were lower than that of measured in	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						the baseline. Besides, the measured result after correction of baseline at NMS13, NMS14 and NMS15 were lower than that of the limit level. The Main Contractor was reminded to re-arrange their proposed night-time construction activities especially in quiet construction works to minimize the noise nuisance to nearby residences. The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during night sleeping time.	
COM-2020167	22/02/2021	1823	CCZJV	Dust	22/02/2021	A complainant who did not wish to disclose his identity called 1823 hotline on 22 nd February 2021 regarding the dust nuisance at slip road to Fo Tan Road. A repetitive case with reference no. 3-6566315922 was referred to the Main Contractor of the captioned Project and ET on 23 rd February 2021. According to the complainant, the dust nuisance concerned at day time was at the slip road to Fo Tan Road near Zone 5 works area. According to the Main Contractor, the major day time construction works at Zone 5 works area in February 2021 was mini-piling works. Regular movement of vehicle for transportation was also carried out on site. Thus, the complaint was considered to be related to the project. The Main Contractor was reminded to reduce the travelling speed of transportation vehicles on site and plan the schedule of delivery transport in order to minimize the dust impact. The Main Contractor	5/3/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						proposed to reduce the exposed surface by providing covers or paving (e.g. with cement grout) to the newly excavated slope.	
COM-2020168	20/02/2021	1823	CCZJV	Noise	23/02/2021	The complaint was received via 1823 on 20 th February 2021 01:00am concerning about the night-time construction works near Sha Tin Police Station at 19 [^] 20 February 2021. According to the Main Contractor, there was night-time construction works near Sha Tin Police Station (Zone 3 & 4) on 19 [^] 20 February 2021. The major construction works were lane shifting works conducted on 19 [^] 20 February 2021 at night-time under approved road closure setup with in-force Construction Noise Permit (CNP) no.GW-RN0798-020. According to the Main Contractor, since Tai Po Road is the main strategic route, implementation of temporary traffic diversion at day time due to loading and unloading material or plant work or road surface remedial work is not feasible. The concerned night work could only be conducted during off-peak period at night time under temporary traffic diversion to avoid causing traffic congestion. According to the Main Contractor, no concurrent operation of Power Mechanical Equipment (PME) and idling were switched off during the loading and unloading of materials and rubble by manual handling of road surface remedial works. Environmental Team (ET) conduct a regular night-time noise monitoring at all monitoring stations between 23:00 25 th February to 03:00 26 th February 2021. 3.13 The	8/3/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						five noise monitoring stations close to the complaint receiving area of Zone 3 & 4 are NMS13, NMS14, NMS15, NMS16 & NMS26. No exceedance cases were found on ET regular night-time noise monitoring measurement at all noise monitoring stations, especially measured at five noise monitoring stations where locate close to the works area (near Sha Tin Police Station in Zone 3&4), the measured result at NMS15, NMS16 and NMS26 were lower than that of measured in the baseline. Besides, the measured result after correction of baseline at NMS13 and NMS14 were lower than that of the limit level in 55 dB(A). The Main Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0798-20) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during the restricted hour.	
COM-2021-0170	03/03/2021	1823	CCZJV	Dust and Noise	04/03/2021	The complaint on 3rd March 2021 at 1:25 pm complained about the noise, dust nuisance generated and insufficient dust mitigation works during the night-time construction works near King Wo House and Wo Che Estate area. A repetitive case with reference no. 3-6638500887 was referred to the Main Contractor and ET of the captioned project on 4th March 2021. According to the Main Contractor, there was night time road works at King Wo House and Wo Che Estate (Zone 4 & 5) on 3rd March 2021. Thus, the complaint considered to be related to the project.	25/03/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						According to ET investigation, the Main Contractor complied with the CNP No.: GW-RN0798-020, with the permission of using Powered Mechanical Equipment (PMEs). No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix G). The Main Contractor was reminded to close all the doors of the acoustic enclosure, included the "SilentCUBE" for hand-held breaker and metallic enclosure. Consider the dust nuisance, no exceedance cases were found on ET regular air quality monitoring measurement (Appendix F). According to the Main Contractor, vapour was emitted from the bottom of the miller, when the milled asphalt falling from the drop point of the conveyor belt to the dump truck container, fugitive dust was generated. The Main Contractor was reminded to enhance the water spray frequency and keep the road surface wet before milling as the mitigation measures on fugitive dust control.	
COM-2021-0172	03/03/2021	1823	CCZJV	Noise	08/03/2021	The second complaint was received on 3rd March 2021 at 1:40 pm complained about the noise nuisance generated during the night-time construction works near Shatin Pui Ying College area. A repetitive case with reference no. 3-6638578830 was referred to the Main Contractor and ET on 8th March 2021. According to the main contractor, there was a night-construction activity near Shatin Pui Ying College and Wo Che Estate (Zone 4 & 5). Thus, the complaint considered to	25/03/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						be related to the project. According to ET investigation, the Main Contractor complied with the CNP No.: GW-RN0798-020, with the allowed usage of PMEs. No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix G). The Main Contractor was reminded to strictly follow and fully comply with the CNP No.: GW-RN0798-20 conditions and the mitigation measures stipulated in the EM&A Manual when construction activities were operated during the restricted hour. The contractor was also reminded to use a movable noise barrier/blanket to block the line of sight from the engine or noise emission part to the nearby NSRs when using PMEs.	
COM-2021-0193	09/05/2021	1823	CCZJV	Noise	17/05/2021	The complaint was first received on 6 th May 2021 at 9:27 a.m. via FEHD email. The complaint was then referred to 1823 case: 3-6727963845 on 9 th May 2021 at 2:52 p.m. A follow-up complaint was received on 11 th May 2021 at 8:20 a.m. The two complaints were referred from 1823 to CEDD on 14 th May 2021 at 6:26 p.m. The complaint cases was referred from AECOM to ET on 17 th May 2021 at 11:46 a.m. According to the Main Contractor, the major construction works at daytime (08:00-18:00) between 6 th to 11 th May 2021 near Mei Wo House were soil replacement works (involved excavation, loading and unloading of materials and pour the no fine concrete) at the works area 1 (between Wo Che Estate King Wo House and Shatin Pui Ying	27/05/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						school) and demolition of existing central divider works (involved breaking, loading and unloading of materials) at the work area 2 (opposite to Wo Che Estate Man Wo House). The ET regular daytime noise monitoring measurement results of NMS16, NMS17, NMS18, NMS19, NMS20 & NMS26 on 6 th , 7 th , 12 th and 13 th May 2021, no exceedance case found. The noise monitoring results were lower than the noise limit of 75 dB(A) L_{eq} (30 minutes) at the facade of dwellings and 70 dB(A) L_{eq} (30 minutes) at the facades of schools (65 dB (A) during examinations). The Main Contractor installed an acoustic blanket, enclosed at the breaker to minimize the noise impacts to nearby NSRs. The Main Contractor was reminded to maintain the newly implemented noise mitigation measure during breaking works. The Main Contractor was reminded to provide additional mitigation measures to minimize the noise nuisance to the NSRs (similar to night-time construction works) during the construction works, for example moveable noise barrier or blanket to block the line of sight from the engine and noise emission parts to the nearby NSRs.	
COM-2021-0200 and COM-2021-0202	07/06/2021	1823	CCZJV	Noise	08/06/2021	Ms. So, a resident of Wo Che Estate, Mei Wo House complained about the noise generated from the daytime construction work located outside Mei Wo House, the tunnel entrance (direction towards Fo Tan). Until 7 th June 2021, total six complaints were received via 1823 (case: 3-6727963845) from the same complainant.	22/06/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>According to the Main Contractor's daytime working schedule from 12th May to 7th June 2021 at zone 5 were soil replacement works (involved excavation, loading and unloading of materials, pour the no fine concrete and formation of haul road) and demolition of existing central divider works (involved loading and unloading of materials, minor breaking and corning operation). According to CEDD, a reply was sent to Ms. So on 27th May 2021. The Resident Site Staff (RSS) of AECOM contacted the complainant on 7th June 2021 night to explain the detail of upcoming construction work and associated noise mitigation measures to minimize the construction noise arising from the concerned construction work. The complainant was also informed that she could contact the RSS directly if she had any further enquiry in future. ET conducted regular daytime noise monitoring at NMS16-20 and NMS26 monitoring stations on 6th, 7th, 12th, 13th, 17th, 18th, 24th, 25th of May and 4th, 5th, 10th, 11th of June 2021. No exceedance case was found and the noise monitoring results were lower than the noise limit of 75 dB(A) $L_{eq(30 \text{ minutes})}$ at the facade of dwellings and 70 dB(A) $L_{eq(30 \text{ minutes})}$ at the facades of schools (65 dB (A) during examinations). ET reminded the Main Contractor to implement additional mitigation measures to minimize the noise nuisance generated from daytime construction works to the nearby Noise Sensitive Receivers (NSRs). The Main Contractor agreed to</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						install an acoustic blanket, enclosed at the breaker to minimize the noise impact generated from the demolition of central divider works. The Main Contractor was reminded to maintain the noise mitigation measure during the breaking works. The Main Contractor was reminded to provide additional mitigation measures during the construction works to minimize the noise nuisance to the NSRs (similar to nighttime construction works), for example, a temporary moveable noise barrier to lower the noise impact and an acoustic blanket to block the line of sight from the engine and noise emission parts to the nearby NSRs. The Main Contractor was also reminded to display the project hotline number 5613-3367 on-site for public enquiry.	
EN-2021-0094	26/07/2021	EPD	CCZJV	Air (Odour)	27/07/2021	<p>A resident of Paris Park Villa complained about the poor air quality around his living area between 19th and 26th July 2021. He suspected that the odour nuisance may be generated from the construction site's diesel machineries. The complaint was received by the EPD's Regional Office (North) on 26th July 2021 with reference no.: RN17367-21.</p> <p>According to the Main Contractor's daytime working schedule between 19th July and 26th July 2021 involved: (1) Zone 4 and 5 North boundary, the construction activities involved the formation of temporary access, backfilling works for noise barrier stem wall, loading and unloading works. Excavations were mainly performed in</p>	13/08/2021

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>areas EX1 and EX2. (2) Zone 4 and 5 South boundaries, the construction activities involved the noise barrier foundation works and the formation of temporary access. Excavations were mainly performed in areas EX3 and EX4. While rebar fixing and formwork erection were also carried out in EX3 area. For area TW1 in Zone 5 South boundary, tree works were performed. There were no work activities carried out at night-time, Sunday and under the hosting of typhoon signals.</p> <p>According to AECOM's Resident Engineer and the Main Contractor, no particular malpractice was observed during the construction activities at Zone 4 and 5 between 19th and 26th July 2021. According to the Main Contractor, only machineries with valid NRMM labels and regular maintenance are being used on-site. The Main Contractor sent the Ultra-Low Sulphur Diesel (ULSD) sample for laboratory testing since Feb 2019. There is no exceedance of the Sulphur content of more than 0.005% by weight in the past and the latest sample collected on 7th July (Cap. 311I Air Pollution Control (Fuel Restriction) Regulations).</p> <p>No particular finding on odour nuisance was found by the ET's staff when performing air monitoring in AMS 14 Ha Wo Che (close to 73A Ha Wo Che) on 21st and 22nd July 2021. ET also inspected the construction site on 29th July 2021 (between 9:00 to 10:15 a.m., weekly</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>environmental inspection). There was no particular observation on odour nuisance or diesel smell generated from the Non-Road Mobile Machineries (NRMMS) and construction activities in the North and South boundary at Zone 4 and 5. No dark smoke was observed from the excavator, power generator, pilling and pre-drilling machines under operation. ET inspected the area around Paris Park Villa and Ha Wo Che on 29th July 2021 between 10:30 a.m. to 11:30 a.m. There was no particular finding on odour nuisance in AMS14 Ha Wo Che (close to 73A Ha Wo Che). ET reminded the Main Contractor to strictly implement the air pollution control measures and minimize the air pollution impact generated from the construction work activities. The Main Contractor also is reminded that only approved or exempted NRMMS include regulated machines and non-road vehicles with proper labels are allowed to be used in specific activities on-site. The NRMMS should be well maintained. The Main Contractor was also be reminded that odour emissions from construction sites need to be controlled. Potential emission includes particulate matter, diesel and hazardous chemicals need to be considered for their odour impact. Use of ULSD should be maintained and dark smoke emission should be prevented in accordance with the Air Pollution Control (Smoke) Regulation and ETWB TCW 19/2005. The Main Contractor was also be reminded to display the project hotline</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						number 5613-3367 on-site for public enquiry.	
DSD Ref: MS 8/0/CE2815 /0 pt.6	01/09/21	DSD	CCZJV	Water	02/09/21	<p>Drainage Services Department (DSD) issued a notice (Ref: MS 8/0/CE2815/0 pt.6) to the Engineer's Representative (AECOM) after their morning inspection on 1st September 2021 concerning the improperly treated water being discharged from the construction site near Fung Wo Estate of the Project to nearby public stormwater drainage system, and of the consequence of contaminating the watercourse at Shing Mun River. The letter of concern was referred to Environmental Team (ET) on 2nd September 2021 at 3:24 p.m. for investigation.</p> <p>According to the Main Contractor and AECOM, the major construction work at Zone 5 south boundary was mini-pilling works (at the end of August). Two pilling machines were operating either individually or simultaneously. There are approximate 130 nos. of pile planned to be installed, and mini-piling works are scheduled to be finished in January 2022. Originally, one WetSep (TW-WS1) and two sedimentation tanks (ST1 and ST2) were provided for handling the wastewater generated from the pilling works and site surface runoff at the zone 5 south boundary. According to the information report and photo records provided by the Main Contractor, the sedimentation tanks (ST1 and ST2) were filled with muddy water and silt on 1st September 2021.</p>	Expected to be submitted to EPD on early October

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>ET inspected the area at Zone 5 south boundary on 2nd, 9th, 16th and 29th September 2021. Observation, reminders and follow-up action were proposed and monitored by the ET on handling the wastewater generated from piling works and site surface run-off. Moreover, EPIs from EPD conducted the site inspection on 9th and 29th September 2021. The two inspections conducted by the EPIs focused on reviewing the general site condition, wastewater treatment facilities set-up, mitigation measures for preventing muddy water formation, handling the wastewater and surface run-off. Observation, recommendations and reminders proposed by the EPIs and ET are grouped and shown in Appendix M.</p> <p>Rectification have been reported by the Main Contractor according to the observation and recommendation from ET and EPIs on 8th, 17th, 27th September and 6th October 2021. During the 2nd joint site inspection, EPIs agreed the piling works can be restarted. However, EPIs reminded that the 2nd piling machine can only be operated until the 2nd WetSep is functioned properly and the effluent quality is acceptable. EPIs mentioned that follow-up inspection expected to be conducted in early or mid-October, focus on inspecting the wastewater treatment efficiency for piling works, paving of the soil surface, mitigation measures for handling the surface run-off. EPIs also mentioned that surprise inspection may be</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						<p>conducted in the future. According to the AECOM, the pilling work was restarted on 30th September 2021.</p> <p>According to this incident, the Main Contractor was reminded by ET to analyze and review the efficiency of the wastewater treatment system according to the construction activities regularly. The Contractor should provide regular maintenance, water quality testing and related checklist for ET and IEC review during the site inspection. The Main Contractor and related Sub-Contractor was reminded by ET and AECOM that the discharge of effluent needs to fulfil the requirement stated in the Water Discharge License (No. WT00032446 – 2018). AECOM and ET requested the Main Contractor to update the Temporary Drainage Management Plan according to the latest work activities. ET also requested the Main Contractor to update the description of the wastewater mitigation measures inside the Environmental Management Plan (EMP) and Environmental Management Report (EMR) and strictly implement to prevent similar case happen in the future.</p> <p>A follow-up site inspection was conducted by the EPIs at Zone 5 south boundary on 26th October 2021. The EPIs reviewed the site condition, treatment efficiency of the temporary wastewater treatment facilities, mitigation measures to</p>	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Investigation summary & Conclusion	Date of Reply
						prevent muddy water generated from soil surface, discharge points and gullies condition. EPIs commented on the mitigation measure around the discharge point near WetSep TW-WS1. The bunding next to the manhole should be rectified to prevent the inflow of muddy water. EPIs reminded that mitigation measures (such as sandbags and bunding) should be provided for enclosing the area near the piling machine. It is for directing the muddy water into the temporary wastewater treatment system. EPIs also reminded regular maintenance of the temporary wastewater treatment system is needed to ensure the effluent's water quality fulfill the standard of the Water Discharge License.	
EPD ref.: RN25674- 21	28/10/21	EPD	CCZJV	Noise	05/11/21	A complaint about the noise nuisance generated from the night-time construction activities near Man Wo House, Wo Che Estate (from 25 to 28 October 2021, during 2 to 5 a.m.) was received by the EPD Regional Office (North) on 28 October 2021. The complaint was referred from EPD to ET on 5 November 2021. ET is carrying out investigation. The details of the investigation and conclusion are expected to be included in the next monthly EM&A report.	TBC

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Cumulative Statistics on Complaints

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Month	Cumulative Project-to-Date
Air	5	0	5
Noise	27	1	28
Water	3	0	3
Waste	0	0	0
Total	34*	0	35*

*The 1st complaint in March 2021 included both the air and noise parameters, hence the total no. of complaints are deducted by 1.

Cumulative Statistics on Notification of Summons and Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Notification of Summons and Prosecutions This Month	Cumulative Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix M

Summary of Site Audit in the Reporting Month



Summary of Site Audit in the Reporting Month

Parameters	Date		
Air Quality	7 October 2021	Observation: 1. Stockpile of excavated soil should be covered with tarpaulin to prevent dust impact. Also prevent the washing of excavated soil by rainwater (Zone 3, S06).	1. Sandbags and tarpaulin have been provided to minimize / prevent surface runoff or silt leaked to public area (Zone 3).
	15 October 2021	Observation: 1. Decolorized NRMM should be replaced with a new one (Zone 4, S6E1).	1. NRMM label has been replaced (Zone 4).
Noise	No specific observation was identified in the reporting month.		
Water Quality	7 October 2021	Observation: 1. Sandbags and tarpaulin should be provided to prevent muddy water formation, and silt outflow into the highway (Zone 3, S06). 2. Stockpile of excavated soil should be covered with tarpaulin to prevent dust impact. Also prevent the washing of excavated soil by rainwater (Zone 3, S06).	1. Sandbags and tarpaulin have been provided to minimize / prevent surface runoff or silt leaked to public area (Zone 3). 2. Stockpile of excavated soil has been covered (Zone 3).
		Reminder: 1. Water leakage from the barrier was observed. Water accidentally outflow to the highway should be prevented. Mitigation measures such as water collection channel and improve the site practice should be considered (Zone 3, RW6).	-
		Follow-up: 1. New WetSep was settled on-site. The pH meter installed on two WetSepts are functioned properly and the readings fulfil the requirement (pH 6 - 10) stated in the Water Discharge License (Zone 5, south boundary). 2. According to the Main Contractor, only one pilling machine was operated. Follow-up the last time observation, the soil surface next to the gullies are cleaned and being paved. Sandbags and tarpaulin coverage were provided next to the u-channel and site boundary next to the highway (Zone 5, south boundary).	-
	15 October 2021	Observation: 1. Sandbags and tarpaulin should be provided to prevent muddy water formation, and silt outflow into the highway (Zone 3, S06). 2. Blockage and broken surface water collection channel were observed during rainfall. The surface water collection channel should be repaired and maintained its function (Zone 5, south boundary).	1. Sandbags and tarpaulin have been provided to prevent muddy water or silt leaked to public area (Zone 3). 2. Surface water collection channel have been repaired (Zone 5).
	26 October 2021	Observation: 1. Enhance the mitigation measure of bunding around the discharge point near the Wetsep TW-WS1 to prevent the inflow of muddy water (Zone 5, south boundary).	1. Bunding for discharge point has been fixed and enhanced (Zone 5).

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameters	Date		
		Reminder: 1. Mitigation measure for enclosing the area near the piling machine to prevent passage of effluent should be improved with enough sandbags / bunds (Zone 5, south boundary).	-
Chemical and Waste Management	7 October 2021	Observation: 1. Drip tray filled with rainwater should be cleaned. The chemical container and drip tray should be covered to prevent rainfall entering (Zone 3, RW6). Coverage with tarpaulin and provide drip tray for holding the chemical containers are needed (Zone 4, S6E1). 2. General refuse and wastewater generated on-site should be cleaned to minimize odour, pest and litter impacts (Zone 3, RW7).	1. Chemical drum has been removed (Zone 3). Drip tray for the chemical drums has been provided and covered with tarpaulin to prevent stagnant water (Zone 4). 2. Skip has been removed (Zone 3).
	15 October 2021	Observation: 1. Chemical container should be provided with drip tray and covered properly (Zone 4, S6E1).	1. Chemical drum has been removed (Zone 4).
	18 October 2021	Observation: 1. Valve should be added to the drip tray to prevent chemical leakage and soil contamination (Zone 4, S6E1).	1. Plug has been provided in the drip tray (Zone 4).
Land Contamination	No specific observation was identified in the reporting month.		
Landscape and Visual Impact	No specific observation was identified in the reporting month.		
General Condition	No specific observation was identified in the reporting month.		
Permit / Licenses	18 October 2021	Observation: 1. Environmental Permit should be displayed conspicuously at the site entrance/exit for public information (Zone 3, SR6).	1. The Environmental Permit has been displayed (Zone 3).
