

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Report No.: 0064/18/ED/0792A

QUARTERLY EM&A REPORT

June 2023 – August 2023

Client : Civil Engineering and Development
Department, HKSAR


Contract No. : NDO 03/2018

Contract Name : Road Widening and Retrofitting Noise Barriers
on Tai Po Road (Sha Tin Section)

Report No. : 0064/18/ED/0792A

Prepared by : Toby Wan

Reviewed by : Calvin Leung

Certified by : 
Calvin Leung
Environmental Team Leader
Fugro Technical Services Limited



Acuity Sustainability Consulting Limited –
Nature & Technologies (HK) Limited Joint Venture



Our ref: PL-202312015

Unit 2320, Level 23,
Tower I, Metroplaza,
223 Hing Fong Road, Kwai Fong,
N.T., Hong Kong.

Attention: Mr. Joseph YAN

13 December 2023

Dear Joseph,

NE/2017/05

**Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)
Quarterly EM&A Report for June to August 2023**

I refer to the email of the ET regarding to the captioned Quarterly EM&A Report with report No. 0064/18/ED/0792A, I have no adverse comment on it and verify this monthly report according to section 1.9 of the Environmental Permit with Permit No. EP- 463/2013/B.

Yours faithfully,

A handwritten signature in black ink, appearing to be 'Li Wai Ming Kevin'.

Li Wai Ming Kevin
Independent Environmental Checker

cc. CRE – Mr. YU Albert (by email only: albert.yu@aecom.com)
CEDD – Mr. YAN Joseph (by email only: jkcyang@cedd.gov.hk)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Report No.: 0064/18/ED/0792A

TABLE OF CONTENTS

EXECUTIVE SUMMARY	1
1. INTRODUCTION	5
2. SUMMARY OF EM&A REQUIREMENTS AND MONITORING RESULTS	11
3. LANDSCAPE AND VISUAL	16
4. WASTE MANAGEMENT	16
5. SITE INSPECTION	17
6. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	23
7. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	31
8. CONCLUSIONS	32

FIGURES

Figure 1	Project General Layout
Figure 2a	Air Monitoring Locations
Figure 2b	Noise Monitoring Locations

LIST OF APPENDICES

Appendix A	Construction Programme
Appendix B	Project Organization Chart
Appendix C	Action and Limit Levels for Air Quality and Noise
Appendix D	Graphical Presentation of Monitoring Data
Appendix E	Waste Flow Table
Appendix F	Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions
Appendix G	Environmental Mitigation Implementation Schedule (EMIS)



EXECUTIVE SUMMARY

- i. The Civil Engineering and Development Department HKSAR has appointed Fugro Technical Services Limited (FTS) to undertake the Environmental Team services for the Project and implement the EM&A works.
- ii. This is the 19th Quarterly EM&A Report presents the environmental monitoring and audit works for the period between 1 June 2023 and 31 August 2023. As informed by the Contractor, major activities in the reporting period included:

Date	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
Jun 2023	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Foundation Works • Slope Reinstatement and Drainage Works • Noise Barrier Erection Works • Relocation of Existing Fire Hydrants and relating Watermains • Reinstatement of cycling track 	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Erection Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> • Tree Works (preservation / felling/ pruning/ transplantation) • Road surface Maintenance • Reinstatement of footpath and cycle track • Construction of Retaining Wall and Erection of Parapet • Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall • Construction Works for N263 & N264 Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works • Construction Works for Lift no.1 • Construction Works N262 Bridge Deck Widening • Relocation of Existing Fire Hydrants and relating Watermains Noise Barrier Foundation Works + Drainage Works 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier Foundation Works • Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope • Reinstatement Works for Traffic Island • Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains
Jul 2023	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier 	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance 	<ul style="list-style-type: none"> • Tree Works (preservation / felling/ pruning/ transplantation) • Road surface 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



	<p>Foundation Works</p> <ul style="list-style-type: none"> • Slope Reinstatement and Drainage Works • Noise Barrier Erection Works • Relocation of Existing Fire Hydrants and relating Watermains • Reinstatement of cycling track 	<ul style="list-style-type: none"> • Noise Barrier Erection Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains 	<p>Maintenance</p> <ul style="list-style-type: none"> • Reinstatement of footpath and cycle track • Construction of Retaining Wall and Erection of Parapet • Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall • Construction Works for N263 & N264 Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works • Construction Works for Lift no.1 • Construction Works N262 Bridge Deck Widening • Relocation of Existing Fire Hydrants and relating Watermains • Noise Barrier Foundation Works + Drainage Works Pilling Construction Works 	<p>Drainage Works</p> <ul style="list-style-type: none"> • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<p>Drainage Works</p> <ul style="list-style-type: none"> • Noise Barrier Foundation Works • Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope • Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains
Aug 2023	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Foundation Works • Slope Reinstatement and Drainage Works • Noise Barrier Erection Works • Relocation of Existing Fire Hydrants and relating Watermains • Reinstatement 	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Erection Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> • Tree Works (preservation / felling/ pruning/ transplantation) • Road surface Maintenance • Reinstatement of footpath and cycle track • Construction of Retaining Wall and Erection of Parapet • Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall • Construction Works for N263 & N264 	<ul style="list-style-type: none"> • Road surface Maintenance • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> • Road surface Maintenance • Noise Barrier Foundation Works • Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope • Noise Barrier Erection Works • Relocation of Existing Fire Hydrants and

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



	of cycling track		<p>Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works</p> <ul style="list-style-type: none"> • Construction Works for Lift no.1 • Construction Works N262 Bridge Deck Widening • Relocation of Existing Fire Hydrants and relating Watermains • Noise Barrier Foundation Works + Drainage Works • Pilling Construction Works 		relating Watermains Reinstatement of cycling track
--	------------------	--	--	--	--

Breaches of the Action and Limit Levels

- iii. No Action / Limit Level exceedance was recorded for 24-hr and 1-hr TSP at the site area in the reporting quarter.
- iv. Day time construction noise monitoring was carried out in the reporting quarter, no Action / Limit Level exceedance was recorded during the period.
- v. For night time construction noise monitoring, no exceedance cases were recorded between 2300 and 0700 of the next day during the reporting quarter.

Complaint, Notification of Summons and Successful Prosecution

- vi. One complaint was received during June 2023:
 1. A complaint was received by 1823 (CASE#3-7780620261) on 30th June 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Wai Wah Centre.
- vii. Four complaints were received during July 2023:
 1. A complaint was received by 1823 (CASE# 3-7782744454) on 3rd July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Jockey Club Ti-I College.
 2. A complaint was received by EPD (EPD ref. RN14897-23) on 7th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Scenery Court.



3. A complaint was received by EPD (EPD ref.: RN16920-23) on 19th July 2023. The complainant who is concerned about the untreated muddy water discharged from the construction site to the Shing Mun River.
4. A complaint was received by 1823 (CASE#3-7677865059) on 26th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Sui Wo Court.

viii. One complaint was received during August 2023:

1. A complaint was received by 1823 (CASE#3-7875615750) on 31st August 2023. The complainant is concerned about the muddy water flowing out of the construction site near Tai Po Road.

ix. Two non-compliance were found during June 2023. The summaries are listed below:

1. A non-compliance was found by ET on 8th June 2023. Three untreated muddy water discharge were found during the site inspection. At Zone 3, a blue pipe was found and connected with the drainage system, no treatment facility was found near by the pump and blue pipe. At Zone 4, N4, untreated muddy water surface run-off was observed, the water directly discharges into a guile without any treatment. At Zone 4, N4, untreated muddy water discharge was found through the blue pipe to the MTR area, no treatment facility was found near by the pump and blue pipe.
2. A non-compliance was found by ET on 29th June 2023. An untreated muddy water discharge was found during the site inspection. At Zone 4, N4, the pump and blue pipe were found not connected to the sedimentation tank nearby. Untreated muddy water discharge was found through the blue pipe to the MTR area. The illegal discharge was stop by RE and ET immediately.

x. No notification of summons and successful prosecution were received in the reporting period.



1. INTRODUCTION

1.1 Background

1.1.1 Contract No. NE/2017/05 – Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section) (TPR-ST) (hereafter referred as “the Contract”), is the Works Contract involved the construction of road widening and retrofitting noise barriers on TPR-ST.

1.1.2 The Works of road widening on TPR-ST is classified as a designated project (DP) under the Part I of Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap. 499). The scale and scope of DP is classified as below:

- Widening and reconstruction of an approximate 1.2 km long of the existing Tai Po Road (Sha Tin Section) from dual 2-lane to dual 3-lane carriageway; and improvement of the existing Sha Tin Rural Committee Road and its junctions.

1.1.3 The Environmental Monitoring and Audit (EM&A) programme under this Contract is governed by the Environmental Permit (EP) (EP No: EP-463/2013/B) and the updated EM&A Manual (Reference No.: 0064/18/ED/0122D). The Works to be executed under this Contract and corresponding EPs include but not be limited to the following main items:

- (i) Road widening works of TPR-ST:
 - (a) widening of TPR-ST of about 1.1 kilometres between Sha Tin Rural Committee Road (STRCR) and Fo Tan Road from dual two-lane to dual three-lane;
 - (b) modification to the existing diamond interchange at TPR-ST / STRCR (STRCR Interchange);
 - (c) provision of two pedestrian lifts, re-provision of staircase and cycle track ramp at the modified STRCR Interchange;
 - (d) modification of existing cycle track subway no. NS30 near Sha Tin Plaza;
 - (e) modification of the existing footbridge no. NF40 across TPR-ST near Wo Che Street;
 - (f) modification of the existing footbridge no. NF66 near Fung Wo Lane;
 - (g) installation of noise mitigation measures between Citylink Plaza and Mei Wo House of Wo Che Estate;
 - (h) associated drainage works, waterworks, street lighting works and traffic control and surveillance system (TCSS).
- (ii) Retrofitting of noise barriers along TPR-ST:
 - (a) western section between Citylink Plaza and Scenery Court;
 - (b) eastern section between Mei Wo House of Wo Che Estate and Fo Tan Road; and
 - (c) associated drainage works, waterworks and street lighting works.
- (iii) Associated street furniture, road marking, traffic signs, directional signs, services and utilities, and
- (iv) Associated landscaping works.

1.1.4 The location and boundary of the site is shown in **Figure 1**.

1.1.5 This quarterly EM&A report is required under EP-463/2013/B Condition 3.4. It is to report the results and findings of the EM&A programme required in the updated EM&A Manual.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



1.1.6 This is the 19th Quarterly EM&A Report which summarized the impact monitoring results and audit findings for the construction of the road widening and retrofitting noise barriers on Tai Po Road (Sha Tin Section) (TPR-ST) (hereafter referred as “the Project”) within the period between 1 June 2023 and 31 August 2023.

1.2 Project Organization

1.2.1 The project proponent was the Civil Engineering and Development Department, HKSAR (CEDD). AECOM Asia Co. Ltd. (AECOM) was commissioned by CEDD as the Engineer for the Project. Acuity Sustainability Consulting Limited – Nature & Technologies (HK) Limited Joint Venture was commissioned as the Independent Environmental Checker (IEC). China railway – China Railway First Group – Zhen Hua Engineering Joint Venture (CCZJV) was appointed as the main contractor for the construction works under the contract NE/2017/05. Fugro Technical Services Limited (FTS) was appointed as the Environmental Team (ET) by CEDD to implement the EM&A programme for the Project.

1.2.2 The organization structure is shown in **Appendix B**. The key personnel contact names and numbers for the Project are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone
Project Proponent (CEDD)	Senior Engineer	Mr. Joseph Yan	3152 3551
Engineer’s Representative (AECOM)	Chief Resident Engineer	Mr. Albert Yu	2276 0618
IEC (Acuity Sustainability Consulting Limited – Nature & Technologies (HK) Limited Joint Venture)	Independent Environmental Checker	Mr. Kevin Li	9779 2247
Main Contractor (CCZJV)	Site Agent	Mr. S.Y. Wong	9257 8521
	Environmental Officer	Ms. Ymen Wong	5267 6087
ET (FTS)	Environmental Team Leader	Mr. Calvin Leung	3565 4441
	Environmental Team Member	Mr. Toby Wan	3656 4450



1.3 Construction Programme and Activities

1.3.1 The construction of the Project commenced on 29 November 2018 and is expected to complete in 2023. The construction programme is shown in **Appendix A**. A summary of the major construction activities undertaken in the reporting period were:

Date	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
Jun 2023	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Foundation Works • Slope Reinstatement and Drainage Works • Noise Barrier Erection Works • Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Erection Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> • Tree Works (preservation / felling/ pruning/ transplantation) • Road surface Maintenance • Reinstatement of footpath and cycle track • Construction of Retaining Wall and Erection of Parapet • Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall • Construction Works for N263 & N264 Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works • Construction Works for Lift no.1 • Construction Works N262 Bridge Deck Widening • Relocation of Existing Fire Hydrants and relating Watermains Noise Barrier Foundation Works + Drainage Works 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier Foundation Works • Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier Foundation Works • Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope • Reinstatement Works for Traffic Island • Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains
Jul 2023	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Foundation Works 	<ul style="list-style-type: none"> • Trial pits excavation • Road surface Maintenance • Noise Barrier Erection Works • Noise Barrier 	<ul style="list-style-type: none"> • Tree Works (preservation / felling/ pruning/ transplantation) • Road surface Maintenance • Reinstatement of 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier 	<ul style="list-style-type: none"> • Road surface Maintenance • Piling Construction Works + Road Drainage Works • Noise Barrier

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Date	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
	<ul style="list-style-type: none"> Slope Reinstatement and Drainage Works Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<p>Foundation Works</p> <p>Relocation of Existing Fire Hydrants and relating Watermains</p>	<p>footpath and cycle track</p> <ul style="list-style-type: none"> Construction of Retaining Wall and Erection of Parapet Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall Construction Works for N263 & N264 Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works Construction Works for Lift no.1 Construction Works N262 Bridge Deck Widening Relocation of Existing Fire Hydrants and relating Watermains Noise Barrier Foundation Works + Drainage Works Pilling Construction Works 	<p>Foundation Works</p> <ul style="list-style-type: none"> Relocation of Existing Fire Hydrants and relating Watermains Reinstatement of cycling track 	<p>Foundation Works</p> <ul style="list-style-type: none"> Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains
Aug 2023	<ul style="list-style-type: none"> Trial pits excavation Road surface Maintenance Noise Barrier Foundation Works Slope Reinstatement and Drainage Works Noise Barrier Erection Works Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> Trial pits excavation Road surface Maintenance Noise Barrier Erection Works Noise Barrier Foundation Works Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> Tree Works (preservation / felling/ pruning/ transplantation) Road surface Maintenance Reinstatement of footpath and cycle track Construction of Retaining Wall and Erection of Parapet Lift no.2 Installation + SR5 Foundation Works + Construction of [former staircase] Abutment Wall 	<ul style="list-style-type: none"> Road surface Maintenance Noise Barrier Foundation Works Relocation of Existing Fire Hydrants and relating Watermains 	<ul style="list-style-type: none"> Road surface Maintenance Noise Barrier Foundation Works Slope Landscaping Works + Irrigation System for Landscaping + Drainage Works on Slope Noise Barrier Erection Works Relocation of Existing Fire Hydrants and

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Date	Zone 1	Zone 2	Zone 3	Zone 4	Zone 5
	<ul style="list-style-type: none"> Reinstatement of cycling track 		<ul style="list-style-type: none"> Construction Works for N263 & N264 Bridge Deck Widening + Construction of New Abutment Wall + Demolition of Existing Beam/ Slab + Road Diversion + Asphalt Works Construction Works for Lift no.1 Construction Works N262 Bridge Deck Widening Relocation of Existing Fire Hydrants and relating Watermains Noise Barrier Foundation Works + Drainage Works Pilling Construction Works 		<ul style="list-style-type: none"> relating Watermains Reinstatement of cycling track



1.4 Status of Environmental Licences, Notifications and Permits

1.4.1 A summary of the relevant environmental licenses permits and/or notifications on environmental protection for this Contract is presented in **Table 1.2**.

Table 1.2 Relevant Environmental Licenses, Permits and/or Notifications

Environmental License / Permit / Notification	Reference Number	Valid From	Valid Till
Environmental Permit for whole project	EP-463/2013/B	20/12/2016	Nil
Receipt of the notification of construction dust production	Form NA	27/7/2018	Nil
Construction Waste Disposal Account	7031619	17/8/2018	Nil
Chemical Waste Producer Registration	5318-758-C4314-01	06/11/2018	Nil
Effluent Discharge License (Zone 1 – 5)	WT00032446-2018	09/11/2018	30/11/2023
Effluent Discharge License (Shui Chong Street)	WT00033829-2019	25/06/2019	30/06/2024
Construction Noise Permit for 24 hours Water Pump (Zone 1 – 5)	GW-RN0287-23	01/04/2023	30/09/2023
Construction Noise Permit for Road Closure, General Night Works (Zone 1 – 5)	GW-RN0292-23	27/03/2023	26/06/2023
Construction Noise Permit for Road Closure, General Night Works (Zone 1 – 5)	GW-RN0514-23	16/05/2023	15/07/2023
Construction Noise Permit for Road Closure, General Night Works (Zone 1 – 5)	GW-RN0627-23	27/06/2023	26/09/2023
Construction Noise Permit for Road Closure, Erection of Sign Gentry (Zone 1 – 2)	GW-RN0670-23	08/07/2023	30/09/2023
Construction Noise Permit for Central Medium and South Hollow Abatement and N4 (Zone 3 – 5)	GW-RN0735-23	16/07/2023	15/09/2023



2. SUMMARY OF EM&A REQUIREMENTS AND MONITORING RESULTS

2.1 Monitoring Requirement

2.1.1 In accordance with the updated EM&A Manuals, 24-hour & 1-hour Total Suspended Particulates (TSP) level and Leq (30min) at the designated monitoring stations is required. Impact 24-hour and 1-hour TSP monitoring should be carried out at least once every 6 days. Leq (30min) monitoring is conducted for at least once a week during the construction phase between 0700 and 1900 on normal weekdays. The Action and Limit Levels of the air quality monitoring and noise monitoring are given in **Appendix C**.

2.2 Monitoring Locations

2.2.1 The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works. The most updated locations are summarized in **Table 2.1** and shown in **Figure 2a**.

Table 2.1 Location of Air Quality Monitoring

Reporting Period	Monitoring Station	Location	Land uses
Jun 2023	AMS4	Wai Wah Centre (Site Boundary)	Residential Village
	AMS7A	Sheung Wo Che	Residential Village
	AMS12	Fung Wo Estate	Residential Village
	AMS17	Wo Che Estate	Residential Village
Jul 2023	AMS4	Wai Wah Centre (Site Boundary)	Residential Village
	AMS7A	Sheung Wo Che	Residential Village
	AMS12	Fung Wo Estate	Residential Village
	AMS17	Wo Che Estate	Residential Village
Aug 2023	AMS4	Wai Wah Centre (Site Boundary)	Residential Village
	AMS7A	Sheung Wo Che	Residential Village
	AMS12	Fung Wo Estate	Residential Village
	AMS17	Wo Che Estate	Residential Village

2.2.2 According to the updated EM&A Manual, 25 noise monitoring locations were included during the noise monitoring. The most updated locations are summarized in **Table 2.2** and shown in **Figure 2b**.



Table 2.2 Location of Noise Monitoring Station

Monitoring Station	Location	Land Uses	Type of Measurement
NMS1	Scenery Court	Residential	Façade
NMS2	Villa Le Parc	Residential	Façade
NMS3	Hilton Plaza	Residential	Façade
NMS4	Tin Liu	Residential Village	Façade
NMS5A	Wai Wah Centre (Site Boundary)	Residential	Façade
NMS6A	Wai Wah Centre (Site Boundary)	Residential	Façade
NMS7	Tin Liu	Residential Village	Façade
NMS8	Shatin Plaza	Residential	Façade
NMS9	Lek Yuen Estate	Residential	Façade
NMS10A	Shatin Tsung Tsin School	School	Façade
NMS11	Sheung Wo Che	Residential Village	Façade
NMS12	SKH Holy Spirit Primary School	School	Façade
NMS13	Lek Yuen Estate	Residential	Façade
NMS14	Sheung Wo Che	Residential Village	Façade
NMS15	Ha Wo Che	Residential Village	Façade
NMS16	Ha Wo Che	Residential Village	Façade
NMS17	Shatin Pui Ying College	School	Façade
NMS18	Ha Wo Che	Residential Village	Façade
NMS19	Wo Che Estate	Residential	Façade
NMS20	Wo Che Estate	Residential	Façade
NMS23	Pai Tau	Residential Village	Façade
NMS24	Shatin Plaza	Residential	Façade
NMS25A	Sheung Wo Che	Residential Village	Façade
NMS26	Wo Che Estate	Residential	Façade
NMS27	Jockey Club Ti-I College	School	Façade

2.3 Results and Observations

2.3.1 No Action and Limit Level exceedance for 24-hr & 1-hr TSP was recorded in the reporting period at all monitoring stations. The monitoring data of 24-hr and 1-hr TSP are summarized in **Table 2.3 and 2.4**. Graphical presentation of the monitoring data in the reporting period is presented in **Appendix D**.



Table 2.3 Summary of 24-hr TSP Monitoring Results

Monitoring Station	24-hr TSP ($\mu\text{g}/\text{m}^3$) in Reporting Period			Average ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
	Jun 2023	Jul 2023	Aug 2023			
AMS4	34-62	25-47	21-45	37	200	260
AMS7A	38-62	28-50	22-44	40	171	
AMS12	42-66	28-61	22-29	41	168	
AMS17	41-59	27-55	23-29	39	171	

Table 2.4 Summary of 1-hr TSP Monitoring Results

Monitoring Station	1-hr TSP ($\mu\text{g}/\text{m}^3$) in Reporting Period			Average ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
	Jun 2023	Jul 2023	Aug 2023			
AMS4	37-73	30-58	24-54	43	348	500
AMS7A	40-76	28-60	22-59	44	344	
AMS12	41-76	34-65	27-36	45	296	
AMS17	43-69	31-69	24-36	44	338	

- 2.3.2 During the reporting month, major dust sources included trial pits excavation, piling works, demolition of existing parapet, removal of existing staircase, road surface maintenance and ELS works were observed in the site.
- 2.3.3 No Action / Limit Level exceedance for day time construction noise monitoring was recorded in the reporting period at all monitoring stations. The results are summarized in **Table 2.5**. Graphical presentation of the monitoring data in the reporting period is presented in **Appendix D**.



Table 2.5 Summary of Day Time Noise Impact Monitoring Results

Monitoring Station	Leq (30min) Range ,dB(A) in Reporting Period			Leq (30min) Limit Level, dB(A)
	Jun 2023	Jul 2023	Aug 2023	
NMS1	61.4 – 67.0	61.1 – 63.8	61.6 – 66.4	75
NMS2	51.2 – 61.4	53.6 – 61.0	53.7 – 55.3	75
NMS3	61.8 – 67.4	61.8 – 65.5	63.1 – 66.5	75
NMS4	62.3 – 64.6	62.3 – 64.3	64.2 – 65.8	75
NMS5A	68.5 – 70.3	62.7 – 68.6	68.3 – 69.7	75
NMS6A	68.0 – 74.1	66.9 – 72.8	71.8 – 74.6	75
NMS7	60.8 – 64.3	62.2 – 66.8	65.7 – 67.8	75
NMS8	61.8 – 65.1	61.1 – 64.8	64.8 – 67.2	75
NMS9	61.7 – 68.4	64.6 – 67.6	64.7 – 68.3	75
NMS10A	63.2 – 64.9	63.2 – 64.5	64.5 – 66.7	65 & 70 ^[2]
NMS11	60.1 – 62.5	60.4 – 62.7	62.3 – 65.5	75
NMS12	62.3 – 63.9	61.8 – 64.1	63.6 – 66.7	65 & 70 ^[2]
NMS13	60.0 – 65.7	61.2 – 65.7	61.3 – 68.2	75
NMS14	61.4 – 67.2	62.1 – 65.4	59.2 – 65.4	75
NMS15	53.2 – 62.5	56.7 – 64.8	63.1 – 64.8	75
NMS16	55.3 – 62.9	54.8 – 64.5	61.2 – 66.2	75
NMS17	62.8 – 66.1	62.9 – 64.9	61.9 – 68.7	65 & 70 ^{[2][3]}
NMS18	54.4 – 62.7	59.6 – 66.0	63.0 – 67.4	75
NMS19	62.7 – 64.7	62.2 – 64.7	62.6 – 68.7	75
NMS20	62.7 – 64.7	62.8 – 65.1	62.8 – 65.1	75
NMS23	61.5 – 65.0	62.6 – 67.5	62.4 – 64.0	75
NMS24	61.4 – 63.4	62.7 – 64.8	63.3 – 69.3	75
NMS25A	63.1 – 68.3	63.1 – 66.9	66.2 – 67.8	75
NMS26	62.8 – 70.6	66.2 – 70.6	66.2 – 68.7	75
NMS27	61.7 – 66.4	62.9 – 67.1	62.0 – 65.7	65 & 70 ^{[2][4]}

Note: 1. Leq (30min) was measured at day-time (0700-1900) on normal weekdays.
 2. 70 dB (A) for schools and 65 dB (A) for schools during examination period. School calendar of NMS 10A, NMS12, NMS 17 and NMS 27 are provided in the monthly report for reference.



2.3.4 According to the Monthly EM&A reports, no exceedance case was recorded between 2300 and 0700 of the next day during the reporting month. The results are summarized in **Table 2.6**.

Table 2.6 Summary of Night Time Noise Impact Monitoring Results (2300 – 0700)

Monitoring Station	Leq Range ,dB(A) in Reporting Period			Baseline Level, dB(A)	Leq Limit Level, dB(A)
	Jun 2023	Jul 2023	Aug 2023		
NMS 1	58.2 – 59.5	57.8 – 58.8	58.2 – 59.2	61.4	55
NMS 2	52.0 – 53.6	51.0 – 53.4	51.8 – 53.7	49.7	55
NMS 3	59.0 – 63.0	62.8 – 63.6	62.4 – 63.9	70.9	55
NMS 4	56.3 – 61.0	55.5 – 61.1	58.1 – 61.1	62.6	55
NMS 5A	65.9 – 66.6	65.3 – 66.5	65.1 – 66.3	67.9	55
NMS 6A	69.3 – 70.1	68.8 – 70.1	69.5 – 70.1	71.5	55
NMS 7	42.7 – 56.5 ^[2]	53.5 – 58.1	52.6 – 57.2 ^[2]	59.0	55
NMS 8	61.8 – 62.1	61.9 – 62.2	61.8 – 62.4	64.4	55
NMS 9	50.9 – 53.5 ^[2]	51.9 – 52.6 ^[2]	50.6 – 53.1 ^[2]	53.5	55
NMS 11	52.5 – 54.3	52.7 – 54.0	52.3 – 54.5	53.2	55
NMS 13	52.6 – 53.8	52.8 – 54.3	52.5 – 53.7	57.3	55
NMS 14	52.3 – 54.4 ^[2]	49.9 – 53.9 ^[2]	51.8 – 54.4 ^[2]	54.1	55
NMS 15	45.5 – 57.3 ^[2]	55.5 – 58.0	45.5 – 57.6 ^[2]	58.8	55
NMS 16	52.8 – 58.1	54.9 – 58.2	50.8 – 58.2	60.1	55
NMS 18	52.1 – 54.5	53.3 – 55.1	51.9 – 55.0	63.2	55
NMS 19	53.8 – 54.8	53.9 – 57.9	53.9 – 55.2	61.7	55
NMS 20	49.4 – 50.9	50.1 – 53.2	49.9 – 51.0	57.7	55
NMS 23	43.6 – 58.8	46.6 – 59.7 ^[2]	43.6 – 58.2 ^[2]	59.9	55
NMS 24	51.1 – 52.1 ^[2]	52.1 – 54.5 ^[2]	49.7 – 54.5 ^[2]	58.0	55
NMS 25A	54.3 – 57.6	53.2 – 56.7	54.1 – 57.3	59.7	55
NMS 26	57.1 – 60.8	56.7 – 60.8	57.3 – 60.9	61.2	55

Note: 1. $L_{eq(15min)}$ was measured at night-time (2300-0700).
2. When the Average Measured Noise Level is greater than Limit Level and baseline level, Average Construction Noise Level (CNL) will be applied, where

$$\text{Calculated CNL} = 10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

2.3.5 During the reporting period, other factors such as road traffic along Tai Po Road may affect the monitoring results. Major noise sources including road traffic along Tai Po Road was observed which may affect the monitoring results.

2.3.6 According to the onsite observation, no raining was observed and no wind speed over 5 m/s was measured during the noise monitoring.



3. LANDSCAPE AND VISUAL

3.1 Results and Observations

- 3.1.1 Site audits were carried out to monitor and audit the implementation of landscape and visual mitigation measures.
- 3.1.2 No non-compliance was recorded in the weekly Site audits in the reporting period.
- 3.1.3 Observations and recommendations during site audits are summarized in **Table 5.1**.

4. WASTE MANAGEMENT

4.1 Results and Observations

- 4.1.1 C&D materials and wastes sorting were carried out on site. Receptacles were available for C&D wastes and general refuse collection.
- 4.1.2 The amount of wastes generated by the site activities in the reporting period is shown in **Appendix E**.
- 4.1.3 The Contractor was advised to properly maintain on site C&D materials and wastes collection, sorting and recording system and maximize reuse / recycle of C&D materials and wastes. The Contractor was reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.
- 4.1.4 The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.
- 4.1.5 The Contractor was reminded to prevent dust nuisance generated from the construction activities by frequent water spraying and the stockpile of construction materials should be covered to have dust suppression. The Contractor was reminded that no debris or silt should be deposited on the adjacent land and outside the site boundary.
- 4.1.6 The Contractor was reminded to provide sufficient wastewater treatment facilities for handling the muddy water being generated from construction activities. The discharge of wastewater from the site should meet the requirement stated in the Water Discharge License. The Contractor was reminded to review the efficiency and provided maintenance of the wastewater treatment facilities regularly.
- 4.1.7 Observations and recommendations during site audits are summarized in **Table 5.1**.



5. SITE INSPECTION

5.1 Site Inspection

- 5.1.1 Site inspections were carried out weekly to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. A summary of the mitigation measures implementation schedule is provided in **Appendix G**.
- 5.1.2 In the reporting quarter, total 14 weekly site inspections were carried out. 3 of them were the joint inspections with the IEC, ER, the Contractor and the ET.
- 5.1.3 All the follow-up actions requested by Contractor’s ET and IEC during the site inspections were completed as reported by the Contractor. No outstanding issues were reported during the reporting period.
- 5.1.4 Details of observations recorded during the site inspections are presented in **Table 5.1**.

Table 5.1 Observations and Recommendations of Site Audit

Parameter	Date	Observations and Reminders	Follow-up Action Taken
Air Quality	1/6/23	Observation 6: A washing facility should be provided at the entrance. (Zone 4, NB, N08)	Washing facility was provided.
	31/8/23	Observation 2: The cement material should be covered. (Zone 3, S06)	Cement bags were covered.
Noise	No specific observation was identified in the reporting period.		
Water Quality	1/6/23	Observation 1: Sandbags and tarpaulin sheets should be provided around the gullies. (Zone 3, CM & Zone 5, CM)	Abandoned storm drains were filled. / Sandbags were provided.
	1/6/23	Observation 4: Tarpaulin sheets along the water barriers should be replaced. (Zone 4, CM)	Sandbags and tarpaulin sheets were provided.
	8/6/23	Observation 2: Blue pipe was observed and connected with the drainage system (Zone 3, SB) and Blue pipe was observed and connected to the MTR area (Zone 5, NB), no treatment facility was found around the pump and blue pipe. The blue pipe should be removed immediately.	Improper blue pipe was removed.
	8/6/23	Observation 5: The soil along the water barriers should be cleared. (Zone 3, N4)	Soil was be cleared
	8/6/23	Observation 6: Untreated Muddy water discharge was observed. The illegal discharge should be stopped immediately. (Zone 4, NB)	Illegal discharge was stopped immediately.
	8/6/23	Reminder 1: Cut-off drain should be provided at the entrance.	N/A
	15/6/23	Observation 1: Sandbags should be provided around the gullies. (Zone 3, CM)	Sandbags were provided.
	15/6/23	Observation 4: Cut-off drain should be	Cut-off drain was

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameter	Date	Observations and Reminders	Follow-up Action Taken
		provided. Also, a washing facility should be provided for wheel washing. (N18)	provided.
	19/6/23	Reminder 1: Stagnant water inside the drip tray should be cleared to prevent land-contamination. (Zone 3)	N/A
	19/6/23	Reminder 3: Sedimentation tank should be accessible for inspection. (Zone 3)	N/A
	29/6/23	Observation 1: Untreated muddy water discharged should be stopped. (Zone 4, N4)	Untreated muddy water discharge was stopped immediately.
	29/6/23	Observation 2: The contractor is reminded to review the sedimentation tank's capacity to ensure enough time for sediment before any discharge. (Zone 4, N4)	Alum was added to the sedimentation tank to increase wastewater treatment ability.
	29/6/23	Reminder 1: Blue pipes should be removed to prevent any misleading. (Zone 3, SB)	N/A
	29/6/23	Follow-up IEC observation: Muddy water surface run-off still has not stopped during the site inspection. No water pump and pipe were found around the observed location. Untreated muddy water surface run-off should be stopped. (Portion E)	Sandbags were provided to stop the surface run-off.
	6/7/2023	Observation 1: Cut-off drain should be provided at all entrances. (Zone 4 & Zone 5, CM)	Cut off drain was provided
	6/7/23	Observation 3: The sedimentation tank should be cleared to ensure there is enough capacity to treat the muddy water. (Zone 5, CM)	Sedimentation tank was cleared.
	13/7/23	Observation 1: Bunding should be provided for gullies. (Zone 3, CM)	Sandbags were provided.
	13/7/23	Reminder 1: The pipe should be removed to prevent any misleading. (Zone 3, SB)	Blue pipe was removed.
	20/7/23	Observation 1: Mitigation measures should be provided to prevent muddy water surface run-off into the nearby gullies. (Zone 3, CM)	Sandbags and cover was provided to prevent muddy water run-off into gullies
	20/7/23	Reminder 1: The tarpaulin sheets and sandbags along the water barriers should be placed properly. (Zone 3, CM)	N/A

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameter	Date	Observations and Reminders	Follow-up Action Taken
	27/7/23	Reminder 1: The sediment process should be accelerated to ensure enough capacity to cope with the rainy days in the next week.	N/A
	3/8/23	Observation 2: The water discharge should meet the requirement of the discharge license. The contractor is reminded to review the capacity of the sedimentation tank and the sedimentation time. The contractor is reminded to desilting frequently to ensure there is enough volume for the tank. The contractor is recommended to add Alum to speed up the process of sedimentation time. (Zone 3, SB)	Sedimentation tank was clear.
	3/8/23	Observation 4: The sediment outside the water barriers should be cleared. (Zone 3, CM, S18)	Soil stain near water barrier edge was cleared.
	3/8/23	Observation 6: The U-channel should be cleared to prevent waste and sand from being washed into the drainage system. (Zone 3, SB, SR6)	U-channel was cleared.
	10/8/23	Observation 1: Sandbags bunding should be provided for guiles. (Zone 3, SB)	Sandbags were provided.
	10/8/23	Observation 3: The broken sandbag should be replaced. (Zone 4, CM)	Sandbags were replaced.
	10/8/23	Observation 4: The contractor is reminded to review the sediment procedure. (Zone 4, CM) The inlet pipe and outlet pipe should not be placed together. The outlet pump should not be arranged in a position that is too low in the sedimentation tank. The contractor is recommended to use the original outlet of the sedimentation tank.	Blue pipes connected to sedimentation tank were modified.
	31/8/23	Observation 1: The sediment inside the sedimentation tank should be cleared. (Zone 3, S06, & Zone 5, CM)	Sedimentation tanks were cleared.
	31/8/23	Observation 5: The mud along the water barriers should be cleared. Also, sandbags should be provided. (Zone 3, SB, S04)	Cut-off drain was cleared.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameter	Date	Observations and Reminders	Follow-up Action Taken
	31/8/23	Reminder 1: Sandbags should be provided along the school area to prevent the muddy water from flowing into the school. (Zone 3, SB)	N.A
	31/8/23	Reminder 2: The contractor is reminded to review the sedimentation tank to ensure there is enough capacity to handle the adverse weather in the coming days.	N.A
Chemical and Waste Management	1/6/23	Observation 3: Drip trays should be provided for chemical containers. (Zone 4, CM & Zone 5, CM)	Drip tray was provided. / Oil container was removed.
	8/6/23	Observation 1: Drip trays should be provided for the oil drums. (Zone 3, SB)	Oil drums were removed.
	8/6/23	Observation 4: The stagnant water and rocks inside the drip tray should be cleared. (Zone 3, N4)	Stagnant water and rocks inside the drip tray were cleared.
	15/6/23	Observation 2: The stagnant water inside the drip tray should be cleared to prevent land-contamination. (Zone 3, CM)	Stagnant water was cleared.
	15/6/23	Observation 3: Waste should be cleared and an enclosed bin should be provided for good housekeeping. (Zone 4, CM)	Waste was cleared.
	15/6/23	Observation 5: Drips tray should be provided for chemical containers and oil drums. (Zone 5, CM)	Oil drum was removed.
	19/6/23	Observation 1: Drip tray should be provided for Chemical containers. (Zone 3)	Oil drum was removed in Zone 3, CM. Drip tray was provided in Zone 3, SB.
	29/6/23	Observation 3: Drip trays should be provided for chemical containers. (Zone 4, N4 & Zone 5, NB)	Oil containers were removed.
	6/7/23	Observation 2: Stagnant water and oil inside the drip tray should be cleared. Also, drip tray should be provided for chemical containers. (Zone 4 & Zone 5, CM)	Stagnant water was cleared. Drip tray was provided.
	6/7/23	Reminder 1: Good housekeeping should be provided. (Zone 4, CM)	N/A
	20/7/23	Observation 2: Construction waste and general refuse should be cleared regularly. (Zone 3, CM)	Waste was cleared.
	20/7/23	Observation 4: The stagnant water inside the drip tray should be cleared to prevent chemical	Stagnant water was cleared.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameter	Date	Observations and Reminders	Follow-up Action Taken
		leakage. (Zone 4, CM)	
	3/8/23	Observation 1: Oil drums should be removed. (Zone 3, SB)	Oil drums were removed.
	3/8/23	Observation 3: The construction waste should be cleared. (Zone 3, SB)	Waste was cleared.
	10/8/23	Observation 2: Drip tray should be provided for chemical containers. (Zone 3, SB)	Oil containers were removed.
	17/8/23	Observation 2: The construction waste should be cleared regularly. (Zone 3, SB)	Waste was cleared.
	21/8/23	Observation 1: Drip trays should be provided for chemical containers. Also, the empties containers should be removed. (Zone 3, SB)	Chemical containers were removed.
	21/8/23	Observation 2: Segregation and disposal of construction waste and general refuse should be implemented. (Zone 3, SB)	Waste was cleared.
	21/8/23	Observation 3: The contractor is reminded to provide a suitable area for temporary storage of chemical waste. The construction materials in front of the chemical cabinet should be cleared. (Zone 3, SB)	Chemical waste storage area was kept clean.
	31/8/23	Observation 4: The stagnant water inside the drip tray should be cleared. (Zone 3, SB)	Stagnant water was cleared.
Land Contamination	1/6/23	Observation 2: Oil should be cleared as soon as possible. (Zone 4, CM)	The Oil and Stagnant water were cleared.
	1/6/23	Observation 5: The oil and stagnant water should be cleared. (Zone 5, CM)	Oil and Stagnant water were cleared.
	8/6/23	Observation 3: Rock breakers should be placed on tarpaulin sheets. (Zone 3, N4)	The breakers were removed.
	19/6/23	Reminder 2: Tarpaulin sheet should be provided underneath of hydraulic breaker to prevent oil leakage. (Zone 3)	N/A

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameter	Date	Observations and Reminders	Follow-up Action Taken
	6/7/23	Reminder 2: Tarpaulin sheet should be padded under the mechanical parts to prevent oil spills. (Zone 5, CM)	N/A
	13/7/23	Observation 2: Drip trays should be provided for chemical containers. (Zone 3, SB, lift2 & Zone 3, CM)	Oil containers were removed.
	13/7/23	Observation 3: Rock breakers should be placed on the tarpaulin sheet to prevent land contamination. (Zone 3, CM)	Breaker was removed
	27/7/23	Observation 1: Drip tray should be provided for the chemical containers. (Zone 3, SR4)	Oil container was removed.
	3/8/23	Observation 5: The rock breaker should be placed on a tarpaulin sheet to prevent land contamination. (Zone 3, CM, S18)	Rock breaker head was removed.
	17/8/23	Observation 1: Tarpaulin sheets should be padded under the rock breakers to prevent land contamination. (Zone 3, SB& CM)	Rock breaker heads were removed.
	31/8/23	Observation 3: Impermeable sheeting should be provided for the rock breaker to prevent land contamination. (Zone 3, SB)	Rock breaker head was removed.
Landscape and Visual Impact	No specific observation was identified in the reporting period.		
General Condition	No specific observation was identified in the reporting period.		
Permit / Licenses	13/7/23	Observation 4: All copies of the permit should be displayed at the site entrance. (Zone 3, lift 1)	EP was provided.
	20/7/23	Observation 3: The faded NRMM label should be replaced. (Zone 3, CM)	NRMM was replaced.
	27/7/23	Observation 2: The faded NRMM label for the generator and excavator should be replaced. (Zone 4 & 5, N4)	NRMM was replaced.
	10/8/23	Observation 5: The faded NRMM should be replaced. (Zone 5, CM)	NRMM was replaced.



6. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

6.1 Environmental Exceedance

6.1.1 No project-related Action and Limit Level exceedance for 24-hr & 1-hr TSP and day time noise was recorded in the reporting period at all monitoring stations.

6.1.2 For night time construction noise monitoring, no exceedance case was recorded between 2300 and 0700 of the next day during the reporting quarter. Number of exceedance in the reporting period was summarized in **Table 6.1** and **6.2**.

Table 6.1 Summary of Exceedance of Dust Monitoring in Reporting Period

Monitoring Station		Number of exceedance in the reporting period							
		24-hour TSP				1-hour TSP			
		Jun 2023	Jul 2023	Aug 2023	Total	Jun 2023	Jul 2023	Aug 2023	Total
AMS 4	AL	0	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0	0
AMS 7A	AL	0	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0	0
AMS 12	AL	0	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0	0
AMS 17	AL	0	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0	0
Total	AL	0	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0	0



Table 6.2 Summary of Exceedance of Daytime Noise Monitoring in Reporting Period

Monitoring Station ¹	Number of exceedance in the reporting period				Total
	Leq (30min) dB(A)				
	Jun 2023	Jul 2023	Aug 2023		
NMS 1	AL	0	0	0	0
	LL	0	0	0	0
NMS 2	AL	0	0	0	0
	LL	0	0	0	0
NMS 3	AL	0	0	0	0
	LL	0	0	0	0
NMS 4	AL	0	0	0	0
	LL	0	0	0	0
NMS 5A	AL	0	0	0	0
	LL	0	0	0	0
NMS 6A	AL	0	0	0	0
	LL	0	0	0	0
NMS 7	AL	0	0	0	0
	LL	0	0	0	0
NMS 8	AL	0	0	0	0
	LL	0	0	0	0
NMS 9	AL	0	0	0	0
	LL	0	0	0	0
NMS 10A	AL	0	0	0	0
	LL	0	0	0	0
NMS 11	AL	0	0	0	0
	LL	0	0	0	0
NMS 12	AL	0	0	0	0
	LL	0	0	0	0
NMS 13	AL	0	0	0	0
	LL	0	0	0	0
NMS 14	AL	0	0	0	0
	LL	0	0	0	0
NMS 15	AL	0	0	0	0
	LL	0	0	0	0
NMS 16	AL	0	0	0	0
	LL	0	0	0	0
NMS 17	AL	0	0	0	0
	LL	0	0	0	0
NMS 18	AL	0	0	0	0
	LL	0	0	0	0
NMS 19	AL	0	0	0	0
	LL	0	0	0	0
NMS 20	AL	0	0	0	0
	LL	0	0	0	0
NMS 23	AL	0	0	0	0
	LL	0	0	0	0
NMS 24	AL	0	0	0	0
	LL	0	0	0	0
NMS 25A	AL	0	0	0	0
	LL	0	0	0	0
NMS 26	AL	0	0	0	0
	LL	0	0	0	0
NMS 27	AL	0	0	0	0
	LL	0	0	0	0
Total	AL	0	0	0	0
	LL	0	0	0	0



Table 6.3 Summary of Exceedance of Night-time Noise Monitoring in Reporting Period

Monitoring Station ¹	Number of exceedance in the reporting period			Total
	Leq _(15min) dB(A)			
	Jun 2023	Jul 2023	Aug 2023	
NMS 1	0	0	0	0
NMS 2	0	0	0	0
NMS 3	0	0	0	0
NMS 4	0	0	0	0
NMS 5A	0	0	0	0
NMS 6A	0	0	0	0
NMS 7	0	0	0	0
NMS 8	0	0	0	0
NMS 9	0	0	0	0
NMS 11	0	0	0	0
NMS 13	0	0	0	0
NMS 14	0	0	0	0
NMS 15	0	0	0	0
NMS 16	0	0	0	0
NMS 18	0	0	0	0
NMS 19	0	0	0	0
NMS 20	0	0	0	0
NMS 23	0	0	0	0
NMS 24	0	0	0	0
NMS 25A	0	0	0	0
NMS 26	0	0	0	0
Total	0	0	0	0



6.2 Complaints, Notification of Summons and Prosecution

10.2.1 One complaint was received during June 2023. The details are listed below:

- A complaint was received by 1823 (CASE#3-7780620261) on 30th June 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Wai Wah Centre.

According to the Main Contractor, all crane lorry and dump truck drivers were briefed to load all material at the lower level to minimize noise generation.

ET carried out regular night-time noise monitoring on 29th ^ 30th June 2023 at NMS5A, NMS6A and NMS8, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).

ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.

The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.

The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.

10.2.2 Four complaints were received during July 2023. The details are listed below:

- A complaint was received by 1823 (CASE# 3-7782744454) on 3rd July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Jockey Club Ti-I College.

Due to the distance of the concerned area is far from the construction site, the complaint was considered to be non-project related.

ET carried out regular night-time noise monitoring on 29th ^ 30th June 2023 at NMS19, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).

ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.



The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.

The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.

- A complaint was received by EPD (EPD ref. RN14897-23) on 7th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Scenery Court.

According to the Main Contractor, no construction activities were carried out near Scenery Court. The nearest activities were carried out near Wai Wah Centre. Due to the certain distance between the working area and the concerned area, this complaint was considered to be non-project related.

ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.

The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.

The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.

- A complaint was received by EPD (EPD ref.: RN16920-23) on 19th July 2023. The complainant who is concerned about the untreated muddy water discharged from the construction site to the Shing Mun River.

According to the government's info-map, the drainage network of the concerned water outfall is distributed along the Wo Che Street and construction site area Zone 4 is also covered in the network.

According to the Main Contractor, all the work activities were operated with suitable water treatment facilities and no water discharged between 11th July 2023 14th July 2023.

According to AECOM photo records on 12th July 2023, a small amount of muddy water leakage through the sandbag bunding into the manhole at Zone 4 was observed. However, the leakage is not sufficient to form the muddy water discharge at Shing Mun River.



The Main Contractor was reminded to periodic inspection the site situation to ensure all the mitigation measures are effective.

The Main Contractor was reminded that the run-off should be prevented from directly entering the sensitive receivers during the construction works.

The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged.

ET checked that there is no sufficient evidence to prove that the complaint is related to the project.

- A complaint was received by 1823 (CASE#3-7677865059) on 26th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Sui Wo Court.

According to the Main Contractor, the hand-held breaker was used inside the acoustic enclosure.

According to the Main Contractor and AECOM, acoustic barriers were set up in the direction of Wo Che Estate during the construction activities. However, due to the safety reason, the noise barriers cannot set up in the direction of Sui Wo Court.

According to the Main Contractor, refreshment training will be provided to the frontline supervisory staff about the CNP requirements to ensure all the construction activities fulfil all the conditions in the CNP.

ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.

The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.

The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.

10.2.3 A complaint was received during August 2023. The details are listed below:

- A complaint was received by 1823 (CASE#3-7875615750) on 31st August 2023. The complainant is concerned about the muddy water flowing out of the construction site near Tai Po Road.

According to the Main Contractor, the muddy water overflow was the result of the frequent rainstorms that occurred.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



ET checked that the complaint was considered to be related to the project.

The Main Contractor was reminded to provide a site channel, bunds or sandbags as a direct runoff into the sediment traps to prevent muddy water directly discharged to the public area.

The Main Contractor was reminded to periodic inspections of the site to determine compliance with the functioning of onsite surface water collection channels and sediment traps.

The Main Contractor was reminded to review all the capacity of sedimentation tanks on the site to see if they are enough to handle the heavy rain situation.

The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged.

10.2.4 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix F**.



10.2.5 Two non-compliance were found during June 2023. The details are listed below:

- A non-compliance was found by ET on 8th June 2023. Three untreated muddy water discharge were found during the site inspection (Photos are shown in **Appendix O**). At Zone 3, a blue pipe was found and connected with the drainage system, no treatment facility was found near by the pump and blue pipe. At Zone 4, N4, untreated muddy water surface run-off was observed, the water directly discharges into a guile without any treatment. At Zone 4, N4, untreated muddy water discharge was found through the blue pipe to the MTR area, no treatment facility was found near by the pump and blue pipe.

ET checked that the Main Contractor did not comply with the water discharge licence (WT00032446-2018).

According to the Main Contractor, all the illegal discharge point were stop immediately on 8th June 2023. A prevention plan of direct discharge of wastewater was provided by the Main Contractor on 21st June 2023.

The Main Contractor was reminded to wastewater generated from construction site should be treated before any discharge to meet the requirement on the water discharge licence (WT00032446-2018).

The Main Contractor was reminded to review all the temporary drainage system and provided sufficient wastewater treatment facilities before discharge.

- A non-compliance was found by ET on 29th June 2023. An untreated muddy water discharge was found during the site inspection (Photos are shown in **Appendix O**). At Zone 4, N4, the pump and blue pipe were found not connected to the sedimentation tank nearby. Untreated muddy water discharge was found through the blue pipe to the MTR area. The illegal discharge was stop by RE and ET immediately.

ET checked that the Main Contractor did not comply with the water discharge licence (WT00032446-2018).

The Main Contractor was reminded to review the prevention plan that they were provided on 21st June 2023 and submit the temporary drainage system management plan immediately.

The Main Contractor was reminded that all wastewaters should be treated before any discharge to meet the requirements under the water discharge licence.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



7. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

7.1 Implementation Status

7.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting period is summarized in **Appendix G**.



8. CONCLUSIONS

- 8.1.1 No Action and Limit Level exceedance for 24-hr & 1-hr TSP was recorded in the reporting period at all monitoring stations.
- 8.1.2 Day time construction noise monitoring was carried out in the reporting quarter, no Action / Limit Level exceedance was recorded during the period.
- 8.1.3 For night time construction noise monitoring, no exceedance case was recorded between 2300 and 0700 of the next day during the reporting month.
- 8.1.4 Total 14 weekly environmental site inspections were carried out in the reporting period. Recommendations on mitigation measures on air quality, construction noise, water quality, chemical and waste management, land contamination, permit / licenses were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.5 One complaint was received during June 2023:
- A complaint was received by 1823 (CASE#3-7780620261) on 30th June 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Wai Wah Centre.
- 8.1.6 Four complaints were received during July 2023:
- A complaint was received by 1823 (CASE# 3-7782744454) on 3rd July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Jockey Club Ti-I College.
 - A complaint was received by EPD (EPD ref. RN14897-23) on 7th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Scenery Court.
 - A complaint was received by EPD (EPD ref.: RN16920-23) on 19th July 2023. The complainant who is concerned about the untreated muddy water discharged from the construction site to the Shing Mun River.
 - A complaint was received by 1823 (CASE#3-7677865059) on 26th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Sui Wo Court.
- 8.1.7 One complaint was received during August 2023:
- A complaint was received by 1823 (CASE#3-7875615750) on 31st August 2023. The complainant is concerned about the muddy water flowing out of the construction site near Tai Po Road.
- 8.1.8 Two non-compliance were found during June 2023. The summaries are listed below:
- A non-compliance was found by ET on 8th June 2023. Three untreated muddy water discharge were found during the site inspection. At Zone 3, a blue pipe was found and connected with the drainage system, no treatment facility was found near by the pump and blue pipe. At Zone 4, N4, untreated muddy water surface run-off was observed,



the water directly discharges into a gully without any treatment. At Zone 4, N4, untreated muddy water discharge was found through the blue pipe to the MTR area, no treatment facility was found near by the pump and blue pipe.

- A non-compliance was found by ET on 29th June 2023. An untreated muddy water discharge was found during the site inspection. At Zone 4, N4, the pump and blue pipe were found not connected to the sedimentation tank nearby. Untreated muddy water discharge was found through the blue pipe to the MTR area. The illegal discharge was stop by RE and ET immediately.

8.1.9 Referring to the Contractor's information, no notification of summons and successful prosecution was received in the reporting period.

8.1.10 The recommended environmental mitigation measures, as proposed in the EIA reports and EM&A Manuals shall be effectively implemented to minimize the potential environmental impacts from the Project. The EM&A programme would effectively monitor the environmental impacts generated from the construction activities and ensure the proper implementation of mitigation measures.

8.1.11 According to the environmental audit performed in the reporting period, the following recommendations were made:

Air Quality Impact

- A washing facility should be provided at the entrance. (Zone 4, NB, N08)
- The broken sandbag should be replaced. (Zone 4, CM)
- The cement material should be covered. (Zone 3, S06)

Construction Noise Impact

- No specific observation was identified in the reporting month.

Water Quality Impact

- Sandbags and tarpaulin sheets should be provided around the gullies. (Zone 3, CM & Zone 5, CM)
- Tarpaulin sheets along the water barriers should be replaced. (Zone 4, CM)
- Blue pipe was observed and connected with the drainage system (Zone 3, SB) and Blue pipe was observed and connected to the MTR area (Zone 5, NB), no treatment facility was found around the pump and blue pipe. The blue pipe should be removed immediately.
- The soil along the water barriers should be cleared. (Zone 3, N4)
- Untreated Muddy water discharge was observed. The illegal discharge should be stopped immediately. (Zone 4, NB)
- Cut-off drain should be provided at the entrance.
- Sandbags should be provided around the gullies. (Zone 3, CM)
- Cut-off drain should be provided. Also, a washing facility should be provided for wheel washing. (N18)
- Sedimentation tank should be accessible for inspection (at Zone 3)
- Cut-off drain should be provided at all entrances. (Zone 4 & Zone 5, CM)
- The sedimentation tank should be cleared to ensure there is enough capacity to treat the muddy water. (Zone 5, CM)
- Bunding should be provided for gullies. (Zone 3, CM)
- The pipe should be removed to prevent any misleading. (Zone 3, SB)



- Mitigation measures should be provided to prevent muddy water surface run-off into the nearby gullies. (Zone 3, CM)
- The tarpaulin sheets and sandbags along the water barriers should be placed properly. (Zone 3, CM)
- The sediment process should be accelerated to ensure enough capacity to cope with the rainy days in the next week.
- The water discharge should meet the requirement of the discharge license.
The contractor is reminded to review the capacity of the sedimentation tank and the sedimentation time.
The contractor is reminded to desilting frequently to ensure there is enough volume for the tank.
The contractor is recommended to add Alum to speed up the process of sedimentation time. (Zone 3, SB)
- The sediment outside the water barriers should be cleared. (Zone 3, CM, S18)
- The U-channel should be cleared to prevent waste and sand from being washed into the drainage system. (Zone 3, SB, SR6)
- Sandbags bunding should be provided for gullies. (Zone 3, SB)
- The contractor is reminded to review the sediment procedure. (Zone 4, CM)
The inlet pipe and outlet pipe should not be placed together.
The outlet pump should not be arranged in a position that is too low in the sedimentation tank.
The contractor is recommended to use the original outlet of the sedimentation tank.
- The sediment inside the sedimentation tank should be cleared. (Zone 3, S06)

Chemical and Waste Management

- Drip trays should be provided for chemical containers. (Zone 4, CM & Zone 5, CM)
- Drip trays should be provided for the oil drums. (Zone 3, SB)
- The stagnant water and rocks inside the drip tray should be cleared. (Zone 3, N4)
- The stagnant water inside the drip tray should be cleared to prevent land- contamination. (Zone 3, CM)
- Waste should be cleared and an enclosed bin should be provided for good housekeeping. (Zone 4, CM)
- Drips tray should be provided for chemical containers and oil drums. (Zone 5, CM)
- Drip tray should be provided for Chemical containers. (at Zone 3).
- Stagnant water inside the drip tray should be cleared to prevent land- contamination. (at Zone 3).
- Stagnant water and oil inside the drip tray should be cleared. Also, drip tray should be provided for chemical containers. (Zone 4 & Zone 5, CM)
- Good housekeeping should be provided. (Zone 4, CM)
- Construction waste and general refuse should be cleared regularly. (Zone 3, CM)
- The stagnant water inside the drip tray should be cleared to prevent chemical leakage. (Zone 4, CM)
- Oil drums should be removed. (Zone 3, SB)
- The construction waste should be cleared. (Zone 3, SB)
- Drip tray should be provided for chemical containers. (Zone 3, SB)
- The construction waste should be cleared regularly. (Zone 3, SB)
- Drip trays should be provided for chemical containers. Also, the empties containers should be removed. (Zone 3, SB)
- Segregation and disposal of construction waste and general refuse should be implemented. (Zone 3, SB)



- The contractor is reminded to provide a suitable area for temporary storage of chemical waste. The construction materials in front of the chemical cabinet should be cleared. (Zone 3, SB)
- The stagnant water inside the drip tray should be cleared.
(Zone 3, SB)
- The mud along the water barriers should be cleared. Also, sandbags should be provided. (Zone 3, SB, S04)
- Sandbags should be provided along the school area to prevent the muddy water from flowing into the school. (Zone 3, SB)
- The contractor is reminded to review the sedimentation tank to ensure there is enough capacity to handle the adverse weather in the coming days.

Land Contamination

- Oil should be cleared as soon as possible. (Zone 4, CM)
- The oil and stagnant water should be cleared. (Zone 5, CM)
- Rock breakers should be placed on tarpaulin sheets. (Zone 3, N4)
- Tarpaulin sheet should be provided underneath of hydraulic breaker to prevent oil leakage (at zone 3).
- Tarpaulin sheet should be padded under the mechanical parts to prevent oil spills. (Zone 5, CM)
- Rock breakers should be placed on the tarpaulin sheet to prevent land contamination. (Zone 3, CM)
- Drip trays should be provided for chemical containers. (Zone 3, SB, lift2 & Zone 3, CM)
- Drip tray should be provided for the chemical containers. (Zone 3, SR4)
- The rock breaker should be placed on a tarpaulin sheet to prevent land contamination. (Zone 3, CM, S18)
- Tarpaulin sheets should be padded under the rock breakers to prevent land contamination. (Zone 3, SB & CM)
- Impermeable sheeting should be provided for the rock breaker to prevent land contamination. (Zone 3, SB)

Landscape and Visual Impact

- No specific observation was identified in the reporting month.

General Condition

- No specific observation was identified in the reporting month.

Permit / Licenses

- All copies of the permit should be displayed at the site entrance. (Zone 3, lift 1)
- The faded NRMM label should be replaced. (Zone 3, CM)
- The faded NRMM label for the generator and excavator should be replaced. (Zone 4 & 5, N4)
- The faded NRMM should be replaced. (Zone 5, CM)

FUGRO TECHNICAL SERVICES LIMITED


Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 1 Project General Layout

Project Management In-charge: **CHK** / Approved: **CHK** / Designer: **CHK** / Checked: **CHK** / Date: 14/12/18
 Project Management In-charge: **CHK** / Approved: **CHK** / Designer: **CHK** / Checked: **CHK** / Date: 14/12/18
 Project Management In-charge: **CHK** / Approved: **CHK** / Designer: **CHK** / Checked: **CHK** / Date: 14/12/18

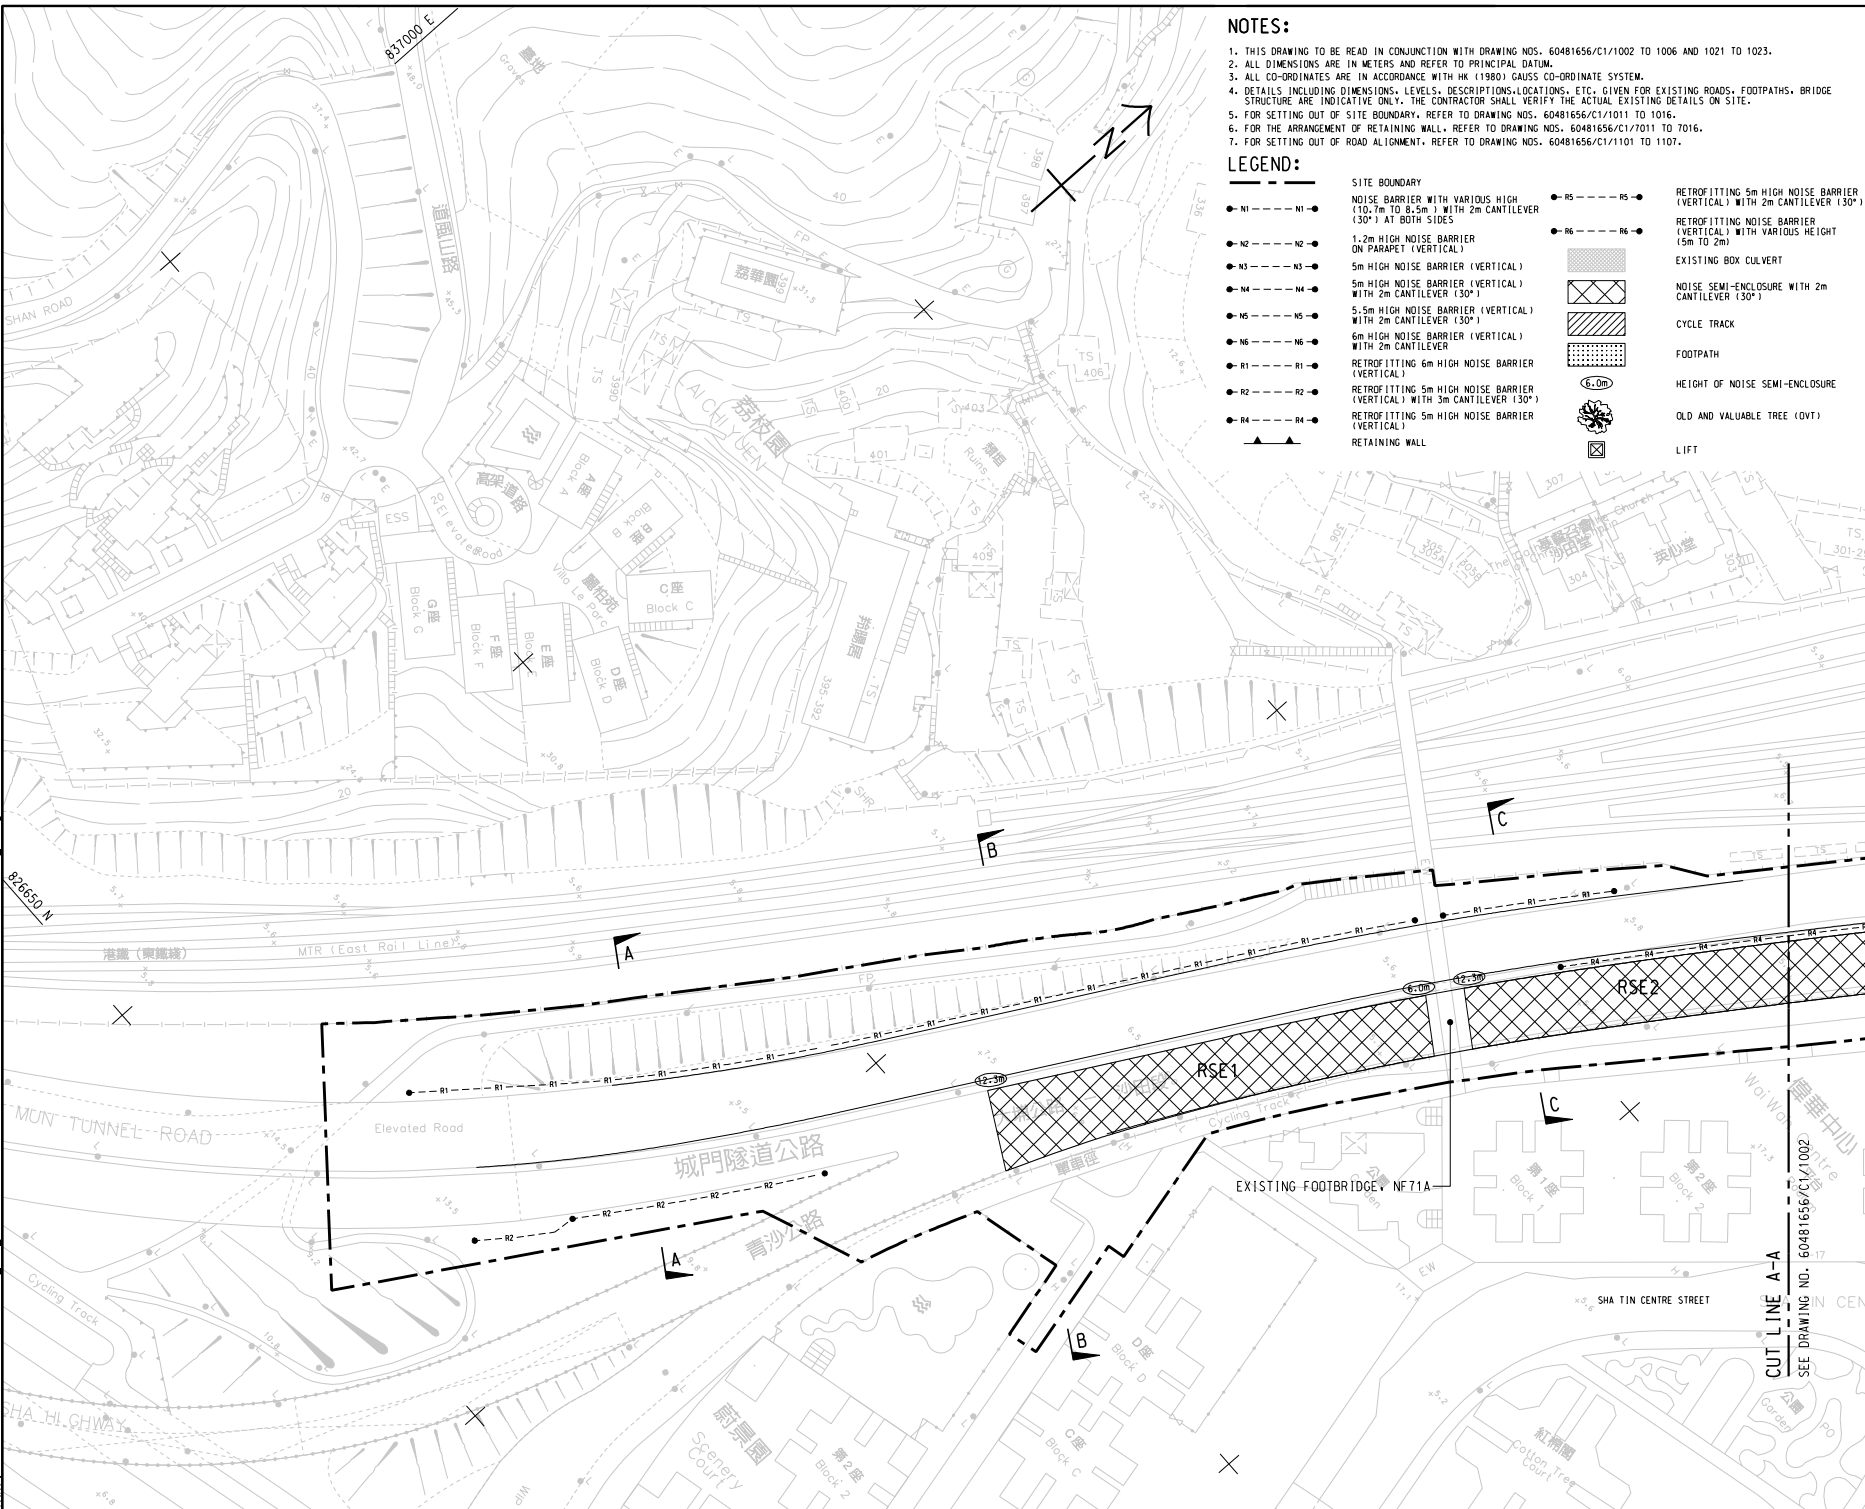

NOTES:

1. THIS DRAWING TO BE READ IN CONJUNCTION WITH DRAWING NOS. 60481656/C1/1002 TO 1006 AND 1021 TO 1023.
2. ALL DIMENSIONS ARE IN METERS AND REFER TO PRINCIPAL DATUM.
3. ALL CO-ORDINATES ARE IN ACCORDANCE WITH HK (1980) GAUSS CO-ORDINATE SYSTEM.
4. DETAILS INCLUDING DIMENSIONS, LEVELS, DESCRIPTIONS, LOCATIONS, ETC. GIVEN FOR EXISTING ROADS, FOOTPATHS, BRIDGE STRUCTURE ARE INDICATIVE ONLY. THE CONTRACTOR SHALL VERIFY THE ACTUAL EXISTING DETAILS ON SITE.
5. FOR SETTING OUT OF SITE BOUNDARY, REFER TO DRAWING NOS. 60481656/C1/1011 TO 1016.
6. FOR THE ARRANGEMENT OF RETAINING WALL, REFER TO DRAWING NOS. 60481656/C1/1011 TO 1016.
7. FOR SETTING OUT OF ROAD ALIGNMENT, REFER TO DRAWING NOS. 60481656/C1/1101 TO 1107.

LEGEND:

- N1 --- N1 ● NOISE BARRIER WITH VARIOUS HIGH (10.7m TO 8.5m) WITH 2m CANTILEVER (30°) AT BOTH SIDES
- N2 --- N2 ● 1.2m HIGH NOISE BARRIER ON PARAPET (VERTICAL)
- N3 --- N3 ● 5m HIGH NOISE BARRIER (VERTICAL)
- N4 --- N4 ● 5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°)
- N5 --- N5 ● 5.5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°)
- N6 --- N6 ● 6m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER
- R1 --- R1 ● RETROFITTING 6m HIGH NOISE BARRIER (VERTICAL)
- R2 --- R2 ● RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL) WITH 3m CANTILEVER (30°)
- R4 --- R4 ● RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL)
- ▲▲▲ RETAINING WALL
- R5 --- R5 ● RETROFITTING 5m HIGH NOISE BARRIER (VERTICAL) WITH 2m CANTILEVER (30°)
- R6 --- R6 ● RETROFITTING NOISE BARRIER (VERTICAL) WITH VARIOUS HEIGHT (5m TO 2m)
- EXISTING BOX CULVERT
- NOISE SEMI-ENCLOSURE WITH 2m CANTILEVER (30°)
- CYCLE TRACK
- FOOTPATH
- HEIGHT OF NOISE SEMI-ENCLOSURE
- OLD AND VALUABLE TREE (OVT)
- LIFT



PROJECT
 ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
 CEDD 土木工程拓展署
 Civil Engineering and Development Department

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com


SUB-CONSULTANTS

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK
1	JAN 18	TENDER DRAWING	BCC

SCALE
 A1: 1:500 METRES

KEY PLAN
 A1: 1:4000



CONTRACT NO.
 NE/2017/05

SHEET TITLE
 GENERAL LAYOUT PLAN
 FIGURE 1.1 b

SHEET NUMBER
 60481656/C1/1001

19/12/2018
 PLOT FILE BY: XE/IB
 DATL: jerry.koh@hstt.com.hk
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN
 ISO A1 841mm x 611mm
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN
 14/12/2018
 PLOT FILE BY: XE/IB
 DATL: jerry.koh@hstt.com.hk
 Project Management In-charge: Designer: FMS/C Checked: BCC Approved: CWN
 ISO A1 841mm x 611mm

NOTE:
 1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/C1/1001.

AECOM

PROJECT
ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
CEDD 土木工程拓展署
 Civil Engineering and Development Department


CONSULTANT
AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS
 24/12/2018

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK	APP
1	JAN 18	TENDER DRAWING	BCC	


SCALE
 A1 1:500 DIMENSION UNIT METRES
 KEY PLAN A1 1:4000




CONTRACT NO.
 NE/2017/05

SHEET TITLE
 GENERAL LAYOUT PLAN
 FIGURE 1.1b

SHEET NUMBER
 60481656/C1/1005

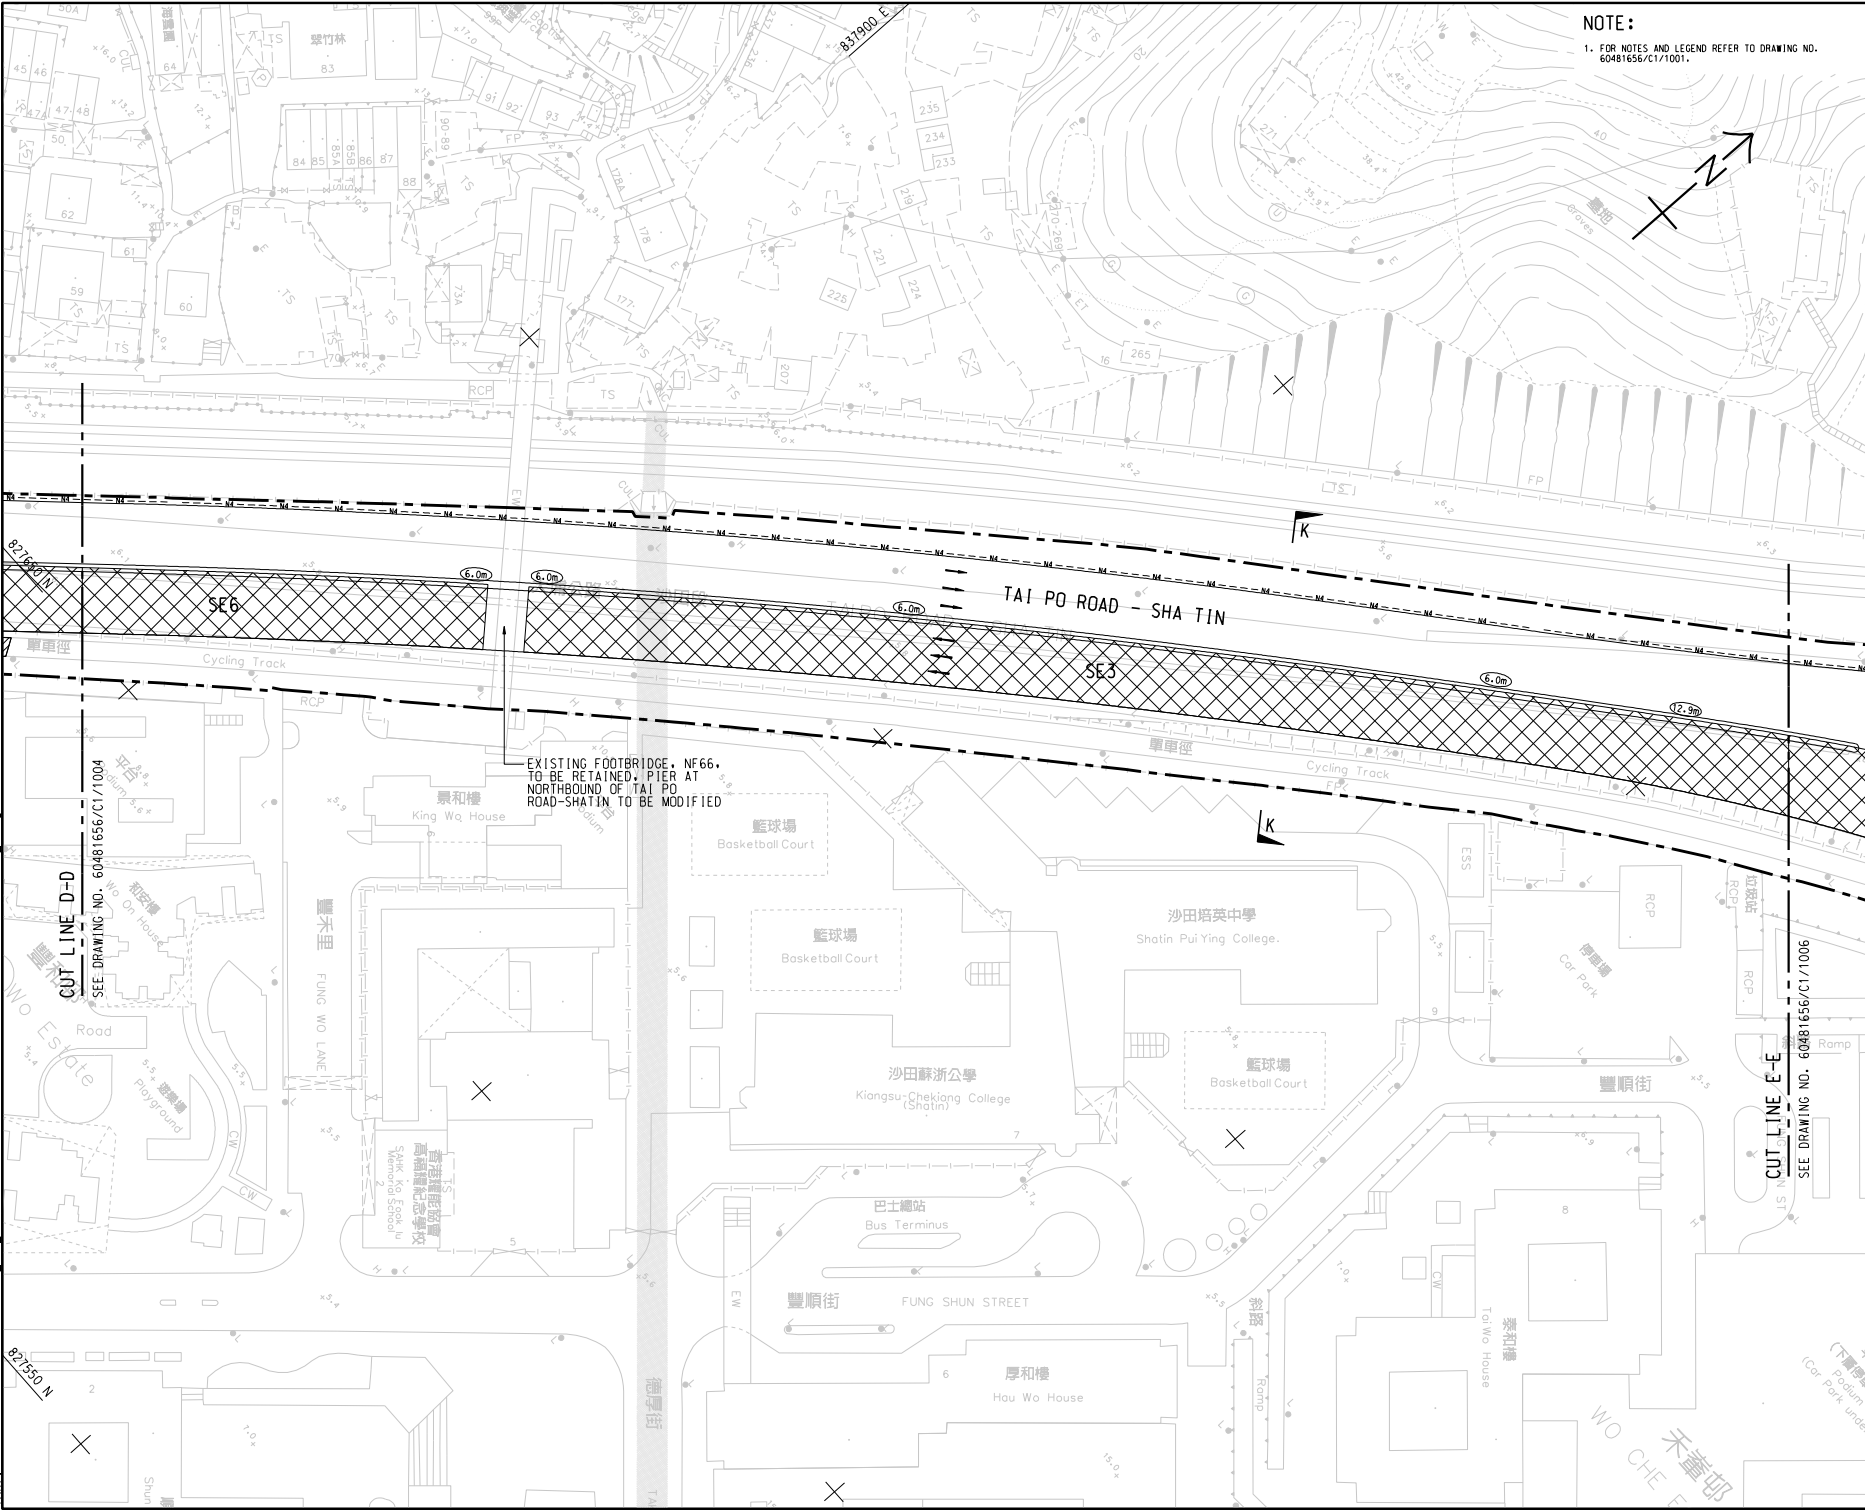

Project Management: H.H.H. / Designer: F.H.S.C. / Checked: B.C.C. / Approved: C.V.N. / Scale: A1 84mm x 84mm / Date: 2/22/2018 / File: D:\aecom\061615 / Path: AECOM\061615\ASB\DWG\CONTRACT\11000\CI_1006.dwg

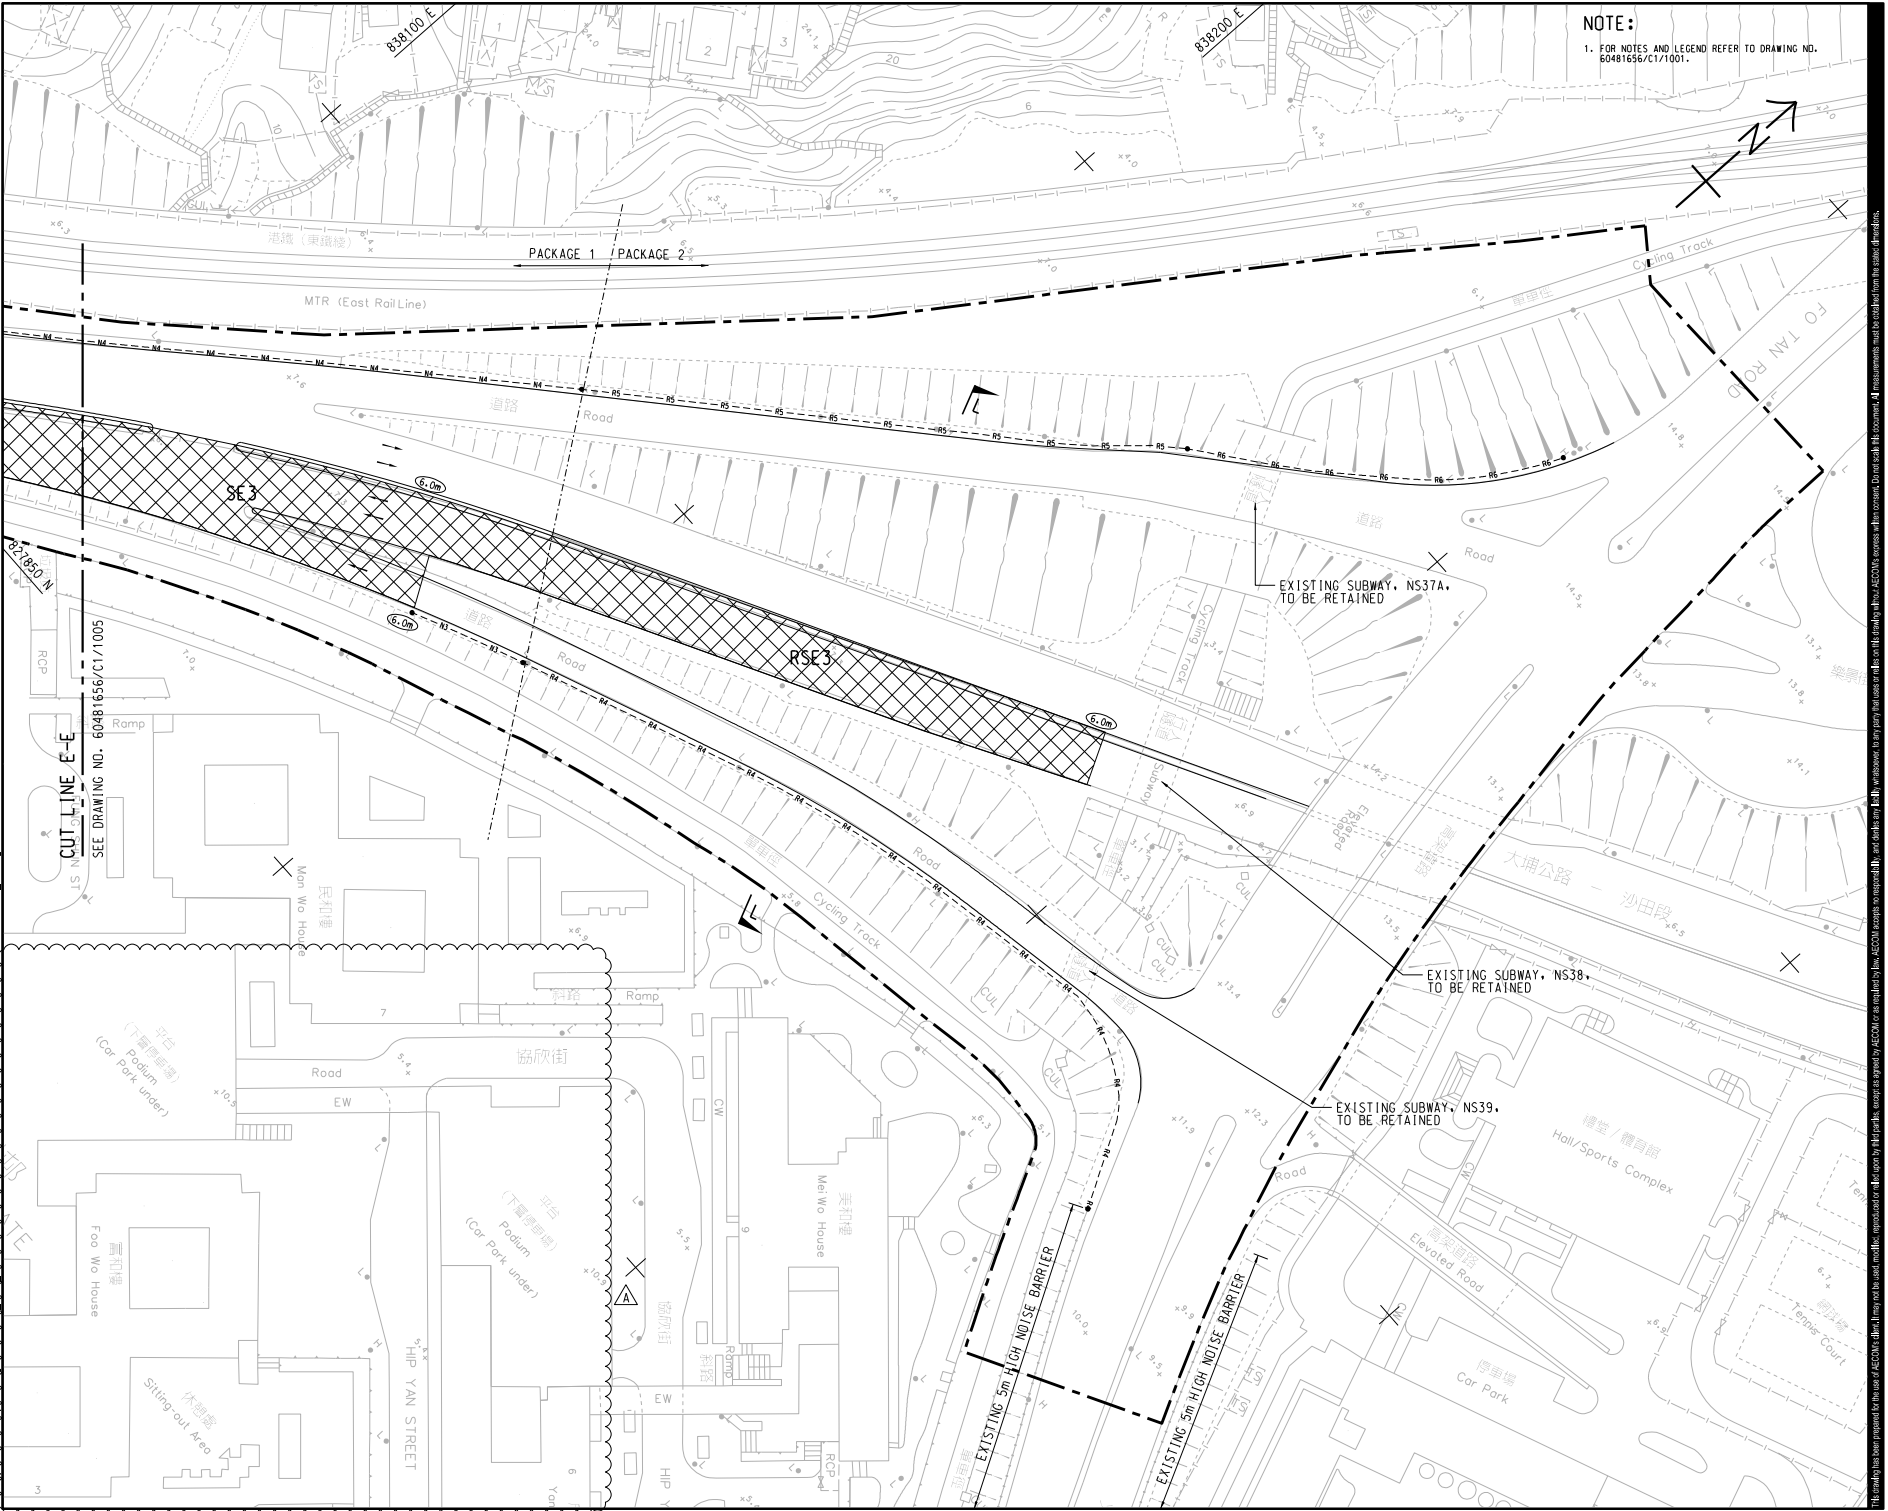

NOTE:
 1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60481656/CI/1001.

AECOM

PROJECT
 ROAD WIDENING AND RETROFITTING NOISE BARRIERS ON TAI PO ROAD (SHA TIN SECTION)

CLIENT
 CEDD 土木工程拓展署
 Civil Engineering and Development Department

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS
 沙利工程顧問公司

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	FEB, 18	TENDER ADDENDUM NO.2	BCC
B	JAN, 18	TENDER DRAWING	BCC
IR	DATE	DESCRIPTION	CHK.
修訂	日期	內容說明	檢核

STATUS
 現狀

SCALE
 比例: A1 1:500

DIMENSION UNIT
 尺寸單位: METRES

KEY PLAN
 大圖比例: A1 1:40000

CONTRACT NO.
 NE/2017/05

SHEET TITLE
 圖則名稱: GENERAL LAYOUT PLAN

FIGURE 1.1b

SHEET NUMBER
 圖則編號: 60481656/CI/1006A

SHEET 6 OF 6

This drawing has been prepared for the use of AECOM and its consultants. It may not be used, modified, reproduced or distributed without the prior written consent of AECOM. AECOM and its consultants shall not be responsible for any errors or omissions in this drawing.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 2a

Air Monitoring Locations

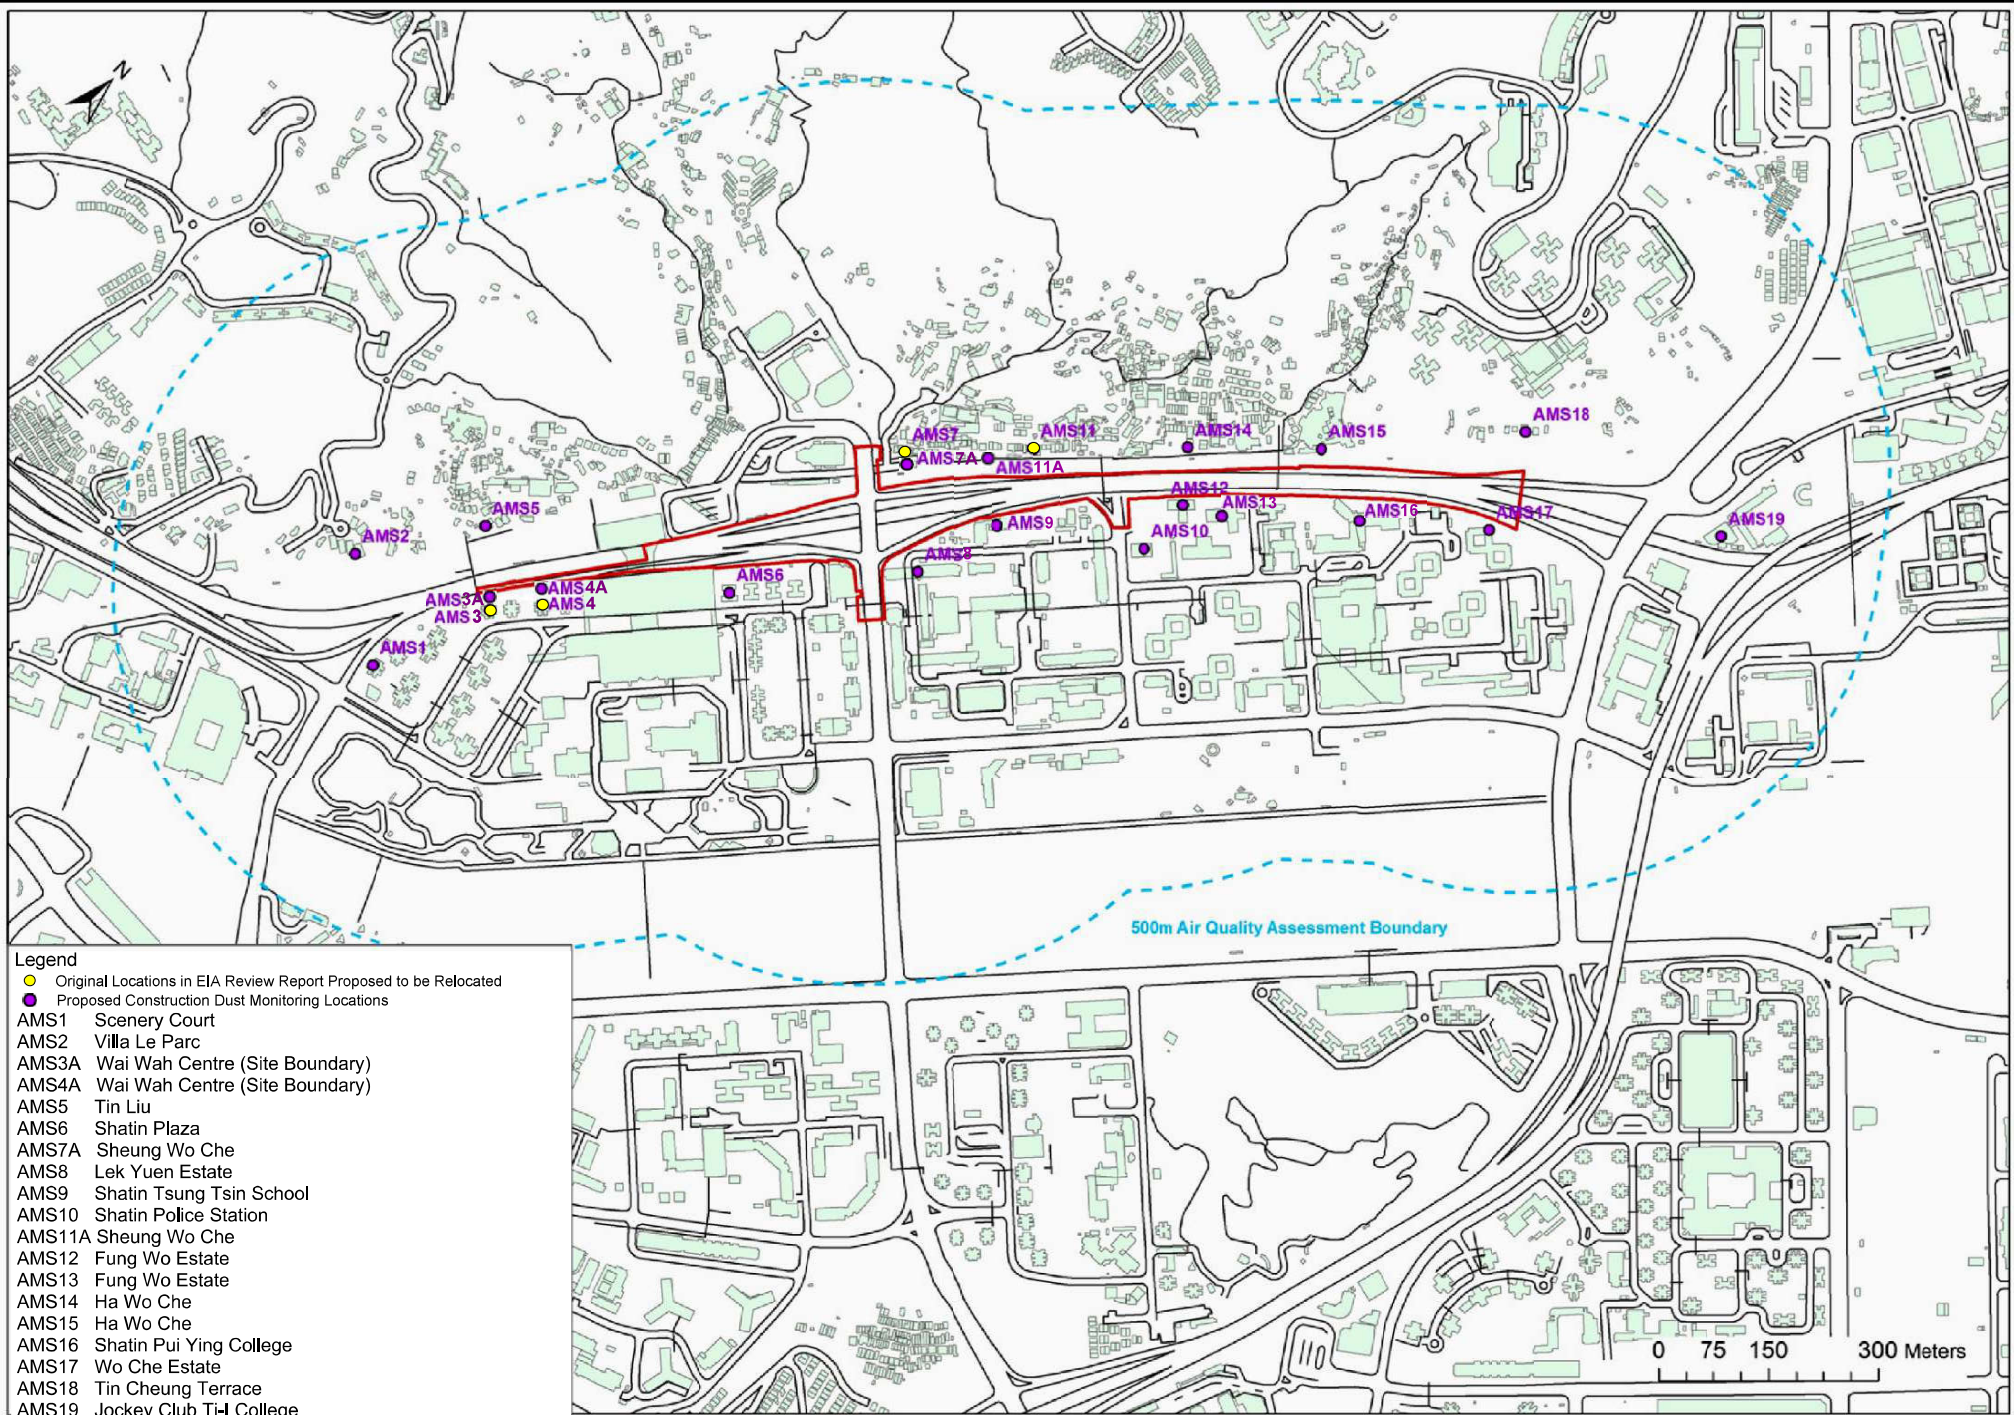


Figure 2a Air Quality Monitoring Locations

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 2b

Noise Monitoring Locations

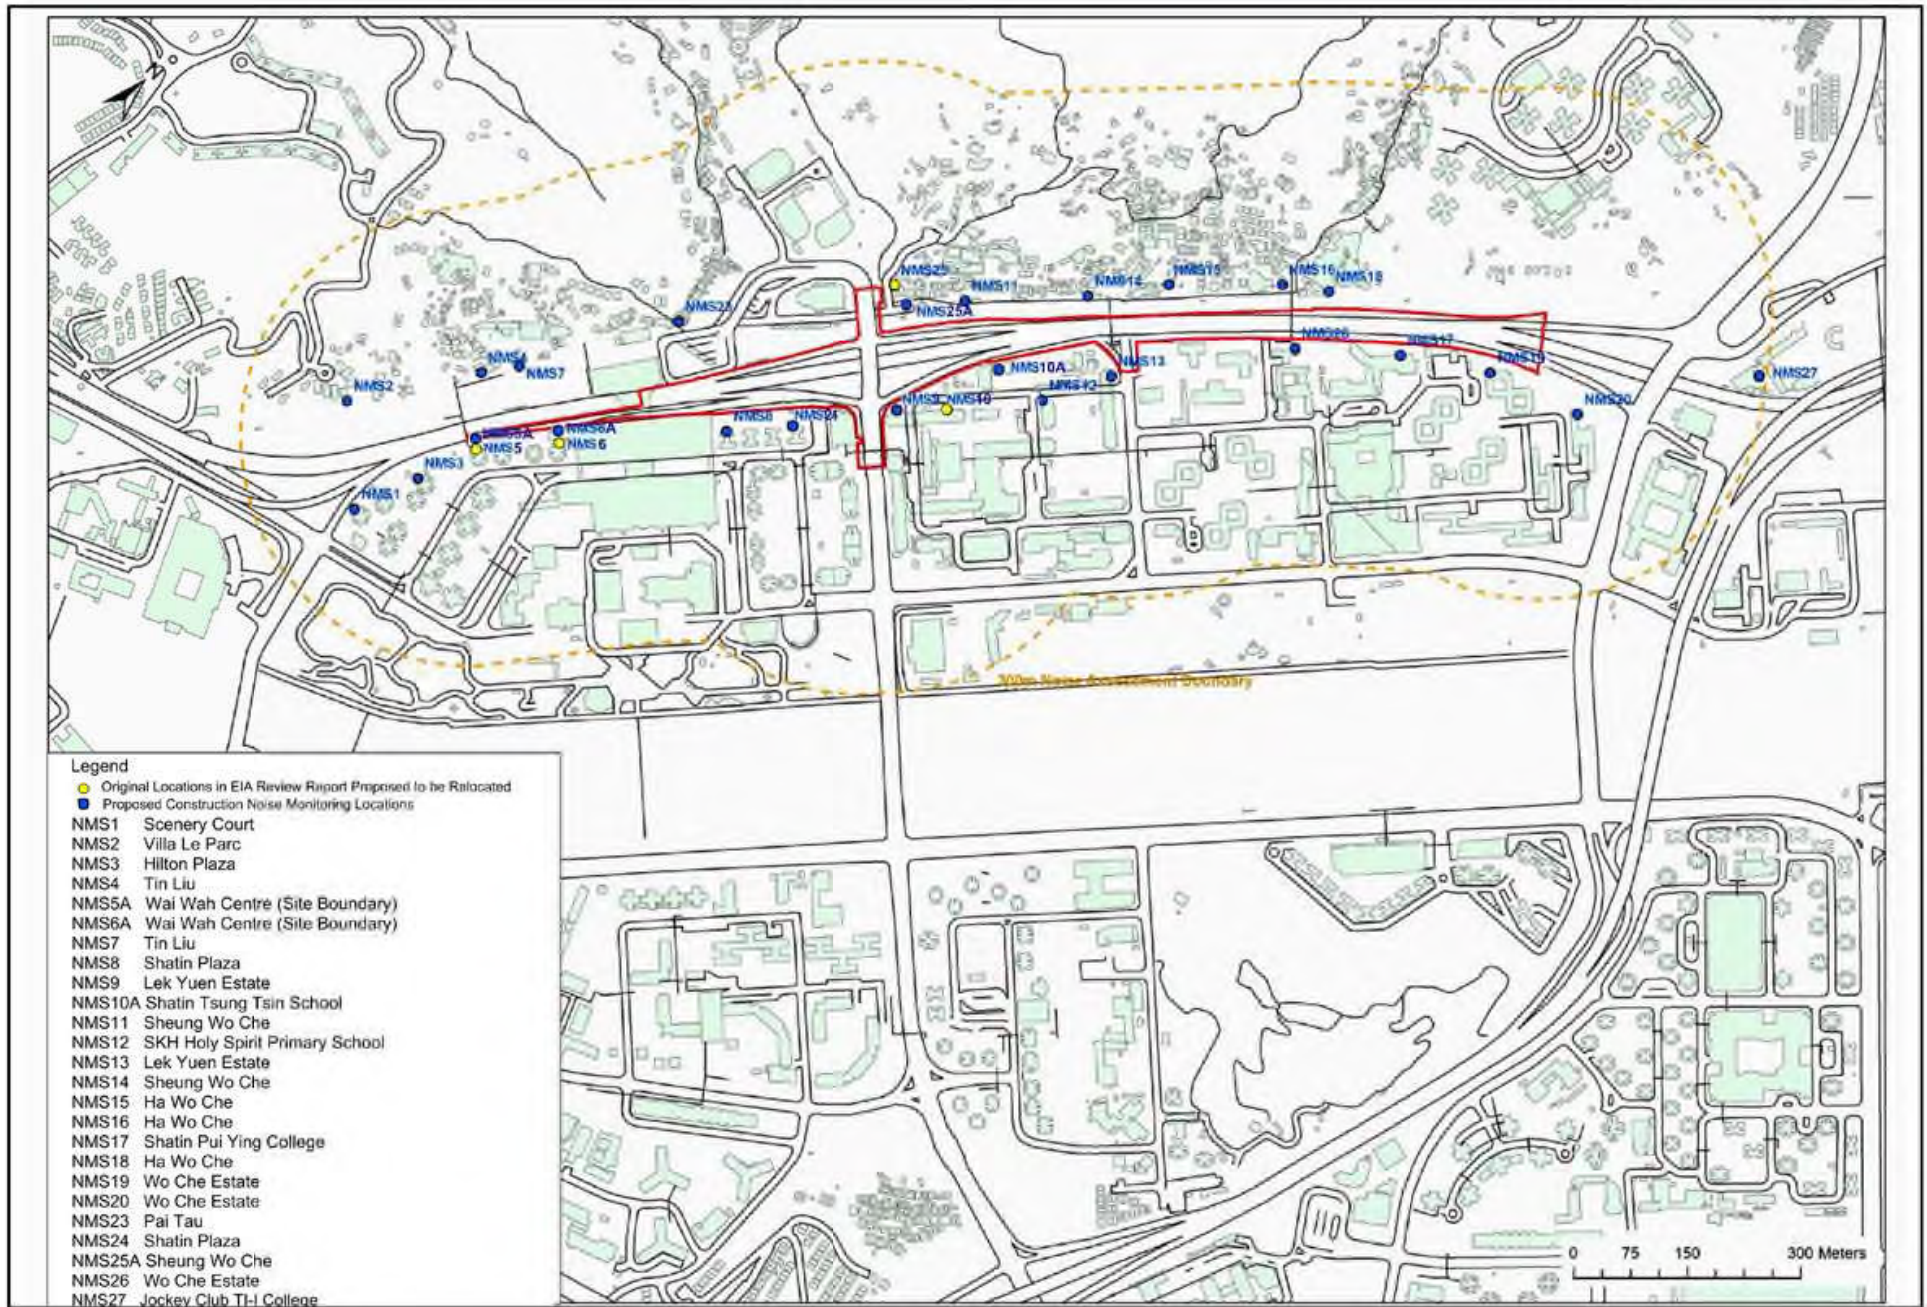


Figure 2b Noise Monitoring Locations

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix A

Construction Programme

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023				
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66
Contract NE_2017_05 3-Months Rolling Programme (base on AP13) August_2023												
PROJECT KEY DATES												
PROJECT COMPLETION												
KEY1142	Target Completion of Section 3 (remaining works)	0	0		31-Aug-23*		28-Jun-22					◆ Target Completion of Section 3 (remaining works),
KEY1150	Contract Completion of Section 3A	0	0		31-Aug-23*		08-Jan-23					◆ Contract Completion of Section 3A,
KEY1160	Target Completion of Section 3A	0	0		31-Aug-23		30-May-23					◆ Target Completion of Section 3A,
DESIGN SUBMISSION												
NOISE MITIGATION MEASURES												
DES1290	PM review & comment	28	1	07-Aug-19 A	31-Aug-23	31-Aug-19	27-Sep-19					PM review & comment
DES1300	Re-submit Superstructure Design of Noise Mitigation Measures in Zone 1 & 2 w/Design Certific.	20	1	26-Aug-19 A	02-Sep-23	12-Sep-21	02-Oct-21					Re-submit Superstructure Design of Noise Mitigation Measures in Zone 1 & 2 w/Design Certificate
DES1310	PM Consent for Construction	28	1	16-Sep-19 A	03-Sep-23	03-Sep-21	30-Sep-21					PM Consent for Construction
DES1330	PM review & comment	28	11	07-Aug-19 A	11-Sep-23	31-Aug-19	27-Sep-19					PM review & comment
DES1340	Re-submit Superstructure Design of Noise Mitigation Measures in Zone 3 w/Design Certificate	21	21	12-Sep-23	03-Oct-23	12-Apr-22	03-May-22					Re-submit Superstructure Design of Noise Mitigation Measures in Zone 3 w/Design Certificate
DES1350	PM Consent for Construction	28	28	03-Oct-23	31-Oct-23	03-May-22	31-May-22					PM Consent for Construction
REMAINING WORKS												
DES1530	PM review & comment	28	1	02-Jan-19 A	31-Aug-23	31-Jan-19	27-Feb-19					PM review & comment
DES1540	Re-submit Design of Watermain & Irrigation System w/Design Certificate	32	1	02-Jan-19 A	31-Aug-23	02-Apr-19	03-May-19					Re-submit Design of Watermain & Irrigation System w/Design Certificate
DES1570	PM review & comment	28	6	18-Oct-22 A	05-Sep-23	05-May-22	01-Jun-22					PM review & comment
DES1580	Re-submit Design of E&M System (E&M & Road Lighting) w/Design Certificate	32	32	06-Sep-23	08-Oct-23	03-Jun-22	04-Jul-22					Re-submit Design of E&M System (E&M & Road Lighting) w/Design Certificate
DES1590	PM Consent for Construction	28	28	08-Oct-23	05-Nov-23	05-Jul-22	01-Aug-22					PM Consent for Construction
WORK BETWEEN SHING MUN TUNNELS ROAD AND FOOT BRIDGE NF71A (ZONE 1)												
PRELIMINARIES WORKS												
SUMMARY PROGRAMME												
Z1SU1032	Zone 1 Stage 1 R1 structure R1-01 to 05	268	0	28-Jul-20 A	31-Aug-23	31-Jul-20	26-Jun-21					Zone 1 Stage 1 R1 structure R1-01 to 05
Z1SU1034	Zone 1 Stage 1 R2 structure	435	0	20-Feb-20 A	19-Jan-23 A	20-Mar-20	07-Sep-21					Zone 1 Stage 1 R2 structure
Z1SU1040	Zone 1 Stage 2 RES1 SB foundation/stem wall	216	6	19-Jan-22 A	07-Sep-23	09-Mar-22	28-Nov-22					Zone 1 Stage 2 RES1 SB foundation/stem wall
Z1SU1042	Zone 1 Stage 2 R1 structure R1-06 to 17	139	16	11-May-22 A	18-Sep-23	25-Apr-22	10-Oct-22					Zone 1 Stage 2 R1 structure R1-06 to 17
Z1SU1050	Zone 1 Stage 3 RES1 Arch beam & panel	52	67	19-Aug-23 A	20-Nov-23	11-Oct-22	29-Nov-22					Zone 1 Stage 3 RES1 Arch beam & panel
NOISE BARRIER AND SEMI-ENCLOSURE												
PILE CAP AND FOOTING												
NORTHBOUND												
Z1_1012	R1_footing/stem wall construction R1-06 to R1-17 (8nr)	72	0	21-May-22 A	21-Aug-23 A	21-May-22	16-Aug-22					R1_footing/stem wall construction R1-06 to R1-17 (8nr)
Z1_1020	R1_backfill & remove ELS	20	3	16-Nov-22 A	06-Sep-23	16-Aug-22	08-Sep-22					R1_backfill & remove ELS
SOUTHBOUND												
Z1_1030	R1_erect steel posts PA1 to PA58 (58nr)	15	3	03-Feb-23 A	11-Sep-23	08-Sep-22	29-Sep-22					R1_erect steel posts PA1 to PA58 (58nr)
Z1_1200	RSE1_erect steel posts PD1 to PD22a (23nr)	6	1	05-Aug-23 A	07-Sep-23	30-Sep-22	11-Oct-22					RSE1_erect steel posts PD1 to PD22a (23nr)
Z1_1210	RSE1_erect steel arch beam PC/D1 to PC/D22 (22nr)	11	7	19-Aug-23 A	25-Sep-23	11-Oct-22	07-Nov-22					RSE1_erect steel arch beam PC/D1 to PC/D22 (22nr)
NOISE BARRIER PANEL												
NORTHBOUND												
Z1_1040	R1_install noise barrier panel PA1 to PA58 (1120 sq.m)	6	5	28-Jun-23 A	18-Sep-23	29-Sep-22	10-Oct-22					R1_install noise barrier panel PA1 to PA58 (1120 sq.m)
SOUTHBOUND												
Z1_1220	RSE1_install noise barrier wall panel PD1 to PD22a (884 sq.m)	5	5	03-Oct-23	10-Oct-23	07-Nov-22	14-Nov-22					RSE1_install noise barrier wall panel PD1 to PD22a (884 sq.m)
Z1_1230	RSE1_install noise barrier roof panel PC/D1 to PC/D22a (1095 sq.m)	11	11	03-Nov-23	20-Nov-23	14-Nov-22	29-Nov-22					RSE1_install noise barrier roof panel PC/D1 to PC/D22a (1095 sq.m)
ROADWORKS AND REMAINING WORKS												
ROADWORKS												
NORTHBOUND												
Z1_1250	Zone 1_road surfacing with flexible pavement Type 1 1391m2	16	16	21-Nov-23	12-Dec-23	25-Oct-22	16-Nov-22					Zone 1_road surfacing with flexible pavement Type 1 1391m2
SOUTHBOUND												
ROADLIGHTING & E&M WORKS												
NORTHBOUND												
Z1_1470	Zone 1_FVMS gantry	30	30	25-Sep-23	02-Nov-23	07-Nov-22	12-Dec-22					Zone 1_FVMS gantry









Remaining Level of Effort	Remaining Work	Milestone	Baseline Milesto...
Actual Level of Effort	Critical Remaining Work	Baseline Milesto...	
Actual Work	Primary Baseline		

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

1 of 6

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023					
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66	
Z1_1480	Zone 1_street lighting & E&M works	45	45	06-Nov-23	29-Dec-23	07-Nov-22	31-Dec-22						
SOUTHBOUND													
Z1_1460	Zone 1_street lighting & E&M works	45	45	06-Nov-23	29-Dec-23	07-Oct-22	29-Nov-22						
GEO TECHNICAL WORKS													
NORTHBOUND													
Z1_1320	Zone 1_fill replacement by no-fines concrete 7SW-D/FF156 (open excavation) NB_R1	52	26	16-Dec-22 A	30-Sep-23	12-Aug-22	15-Oct-22						
WORK BETWEEN FOOT BRIDGE NF71A AND CITYLINE PLAZA (ZONE 2)													
PRELIMINARIES WORKS													
SUMMARY PROGRAMME													
Z2SU1010	Construction Zone 2_Stage 2 RSE2 SB foundation/stem wall	204	5	22-Dec-21 A	06-Sep-23	31-Dec-21	07-Sep-22						
Z2SU1020	Construction Zone 2_Stage 3 RSE2 Arch beam & panel	64	53	09-Jun-23 A	03-Nov-23	01-Aug-22	09-Nov-22						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE CAP AND FOOTING													
SOUTHBOUND													
Z2_1110	RSE2_backfill & remove ELS	29	3	01-Sep-22 A	02-Sep-23	09-Jun-22	14-Jul-22						
STRUCTURE STEEL FRAME													
SOUTHBOUND													
Z2_1130	RSE2_erect steel posts PD23a to PD67 (46nr)	12	2	30-Mar-23 A	06-Sep-23	14-Jul-22	01-Aug-22						
Z2_1140	RSE2_erect steel arch beam PC/D23 to PC/D67 (45nr)	23	9	09-Jun-23 A	16-Sep-23	01-Aug-22	21-Sep-22						
NOISE BARRIER PANEL													
CENTRAL BARRIER													
Z2_1150	RSE2_install noise barrier wall panel PC23 to PC67 (624 sq.m)	4	4	26-Jul-23 A	21-Sep-23	21-Sep-22	27-Sep-22						
SOUTHBOUND													
Z2_1160	RSE2_install noise barrier wall panel PD23a to PD67 (1560 sq.m)	8	6	25-Jul-23 A	03-Oct-23	27-Sep-22	10-Oct-22						
Z2_1170	RSE2_install noise barrier roof panel PC/D23 to PC/D67 (2187 sq.m)	22	22	03-Oct-23	03-Nov-23	10-Oct-22	09-Nov-22						
ROADWORKS AND REMAINING WORKS													
ROADWORKS													
NORTHBOUND													
Z2_1180	Zone 2_road surfacing with flexible pavement Type 1 1562m2	11	11	06-Nov-23	20-Nov-23	10-Oct-22	25-Oct-22						
ROADLIGHTING & E&M WORKS													
NORTHBOUND													
Z2_1315	Zone 2_sign gantry installation NT3954	30	30	16-Sep-23	25-Oct-23	21-Sep-22	28-Oct-22						
Z2_1320	Zone 2_street lighting & E&M works	60	60	06-Nov-23	17-Jan-24	29-Sep-22	10-Dec-22						
SOUTHBOUND													
Z2_1300	Zone 2_sign gantry installation TGS 7	30	30	16-Sep-23	25-Oct-23	21-Sep-22	28-Oct-22						
Z2_1310	Zone 2_street lighting & E&M works	60	60	06-Nov-23	17-Jan-24	10-Oct-22	19-Dec-22						
WORK BETWEEN CITYLINE PLAZA AND FOOTBRIDGE NF40 (ZONE 3)													
PRELIMINARIES WORKS													
SUMMARY PROGRAMME													
Z3SU5000	Zone 3a (TPR area) Stage 1 RW6, RW7 & SR4	354	0	20-Nov-19 A	14-Nov-22 A	02-Sep-19	10-Nov-20						
Z3SU5020	Zone 3a (TPR Area) Stage 3 SE1, SE2, N1, SE4 & SE5 CM foundation	100	63	27-Feb-23 A	15-Nov-23	27-Oct-22	14-Mar-23						
Z3SU5040	Zone 3b (SB near SR6) Stage 1 Construct Lift Tower 2 & staircase	256	0	31-Mar-20 A	21-Jun-23 A	29-Jun-20	11-May-21						
Z3SU5050	Zone 3b (near SR6) Stage 1 SE8 and SR6 foundation and N262 bridge	344	41	02-Jun-20 A	19-Oct-23	26-Jan-21	25-Mar-22						
Z3SU5060	Zone 3b (near SR6) Stage 2 N263 bridge deck construction	487	114	31-Mar-21 A	17-Jan-24	09-Jun-21	30-Jan-23						
Z3SU5070	Zone 3b (near SR6) Stage 3 Construct SR5	682	144	28-Oct-20 A	24-Feb-24	01-Dec-20	21-Mar-23						
Z3SU5080	Zone 3b (near SR6) Stage 4 cycle track ramp	233	233	21-Sep-23	08-Jul-24	08-Oct-22	29-Nov-23						
Z3SU5100	Zone 3c (near SR3) Stage 1 construct RW1, SR3 & subway NS30	162	0	02-Dec-20 A	25-Apr-22 A	01-Dec-20	22-Jun-21						
Z3SU5110	Zone 3c (near SR3) Stage 1 SR2 foundation & RW4 410 to 414	106	229	07-Sep-20 A	11-Jun-24	30-Jan-21	15-Jun-21						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE FOUNDATION WORKS													
SOUTHBOUND													
Z3_1514	SE1-1_mini piles for S1E1-51P (6nr ver) (N/B Stag1b + S/B Stage 4)	24	0	24-Jun-23 A	02-Aug-23 A	28-Nov-22	24-Dec-22						
PILE CAP AND FOOTING													
NORTHBOUND													


 Remaining Level of Effort
  Remaining Work
  Milestone
 Actual Level of Effort
  Critical Remaining Work
  Baseline Milesto...
 Actual Work
  Primary Baseline

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

2 of 6

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023				
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66
Z3_1010	N4_footing/stem wall construction N4-01 to N4-11 (11 nr)	108	10	17-Apr-23 A	12-Sep-23	06-Aug-22	13-Dec-22	N4_footing/stem wall construction N4-01 to N4-11 (11 nr)				
Z3_1020	N4_backfill & remove ELS	22	22	12-Sep-23	10-Oct-23	14-Dec-22	11-Jan-23	N4_backfill & remove ELS				
CENTRAL BARRIER												
Z3_1120	SE1-1_pile cap construction S1E1-01P & S1E1-02P (2nr) (N/B Stag1b + S/B Stage 3)	18	0	06-Jul-23 A	11-Aug-23 A	03-Jan-23	26-Jan-23	SE1-1_pile cap construction S1E1-01P & S1E1-02P (2nr) (N/B Stag1b + S/B Stage 3)				
Z3_1130	SE1-1_backfill & remove ELS (N/B Stag1b + S/B Stage 3)	3	2	23-Aug-23 A	09-Sep-23	27-Jan-23	30-Jan-23	SE1-1_backfill & remove ELS (N/B Stag1b + S/B Stage 3)				
Z3_1140	SE1-2_ELS for footing/cap construction S1E2-01P to S1E2-07 (48m_2 side) (N/B Stag1b + S/B Stage 3)	14	0	31-Jan-23 A	09-Aug-23 A	18-Oct-22	02-Nov-22	SE1-2_ELS for footing/cap construction S1E2-01P to S1E2-07 (48m_2 side) (N/B Stag1b + S/B Stage 3)				
Z3_1150	SE1-2_cap/footing construction S1E2-01P to S1E2-07 (7nr) (N/B Stag1b + S/B Stage 3)	72	0	04-Feb-23 A	18-Aug-23 A	23-Nov-22	21-Feb-23	SE1-2_cap/footing construction S1E2-01P to S1E2-07 (7nr) (N/B Stag1b + S/B Stage 3)				
Z3_1170	SE1-2_backfill & remove ELS (N/B Stag1b + S/B Stage 3)	8	4	15-Mar-23 A	13-Sep-23	22-Feb-23	02-Mar-23	SE1-2_backfill & remove ELS (N/B Stag1b + S/B Stage 3)				
Z3_1200	SE1-3_backfill & remove ELS (N/B Stag1b + S/B Stage 3)	7	4	14-Mar-23 A	12-Sep-23	30-Dec-22	07-Jan-23	SE1-3_backfill & remove ELS (N/B Stag1b + S/B Stage 3)				
Z3_1230	SE1-4_backfill & remove ELS (N/B Stag1b + S/B Stage 3)	12	6	22-Mar-23 A	08-Sep-23	01-Mar-23	14-Mar-23	SE1-4_backfill & remove ELS (N/B Stag1b + S/B Stage 3)				
Z3_1240	SE1-5_ELS for footing construction S1E5-01 to S1E5-05 (51m_2 side) (N/B Stag1a + S/B Stage 0)	15	0	16-May-23 A	01-Aug-23 A	11-Aug-22	27-Aug-22	SE1-5_ELS for footing construction S1E5-01 to S1E5-05 (51m_2 side) (N/B Stag1a + S/B Stage 0)				
Z3_1250	SE1-5_footing construction S1E5-01 to S1E5-05 (5nr) (N/B Stag1a + S/B Stage 0)	54	0	02-Jun-23 A	17-Aug-23 A	29-Aug-22	02-Nov-22	SE1-5_footing construction S1E5-01 to S1E5-05 (5nr) (N/B Stag1a + S/B Stage 0)				
Z3_1260	SE1-5_backfill & remove ELS (N/B Stag1a + S/B Stage 0)	9	5	25-Aug-23 A	06-Sep-23	03-Nov-22	12-Nov-22	SE1-5_backfill & remove ELS (N/B Stag1a + S/B Stage 0)				
Z3_1280	SE1-6_pile cap construction S1E6-01P (1nr) (N/B Stag1a + S/B Stage 0)	18	0	15-Jul-23 A	01-Aug-23 A	03-Nov-22	23-Nov-22	SE1-6_pile cap construction S1E6-01P (1nr) (N/B Stag1a + S/B Stage 0)				
Z3_1290	SE1-6_backfill & remove ELS (N/B Stag1a + S/B Stage 0)	3	2	25-Aug-23 A	01-Sep-23	24-Nov-22	26-Nov-22	SE1-6_backfill & remove ELS (N/B Stag1a + S/B Stage 0)				
Z3_1390	SE5-1_ELS for cap/footing construction S5E1-01P to S5E1-04 (56m_2 side) (N/B Stag1b + S/B Stage 0)	16	4	11-Apr-23 A	30-Oct-23	19-Nov-22	08-Dec-22	SE5-1_ELS for cap/footing construction S5E1-01P to S5E1-04 (56m_2 side) (N/B Stag1b + S/B Stage 0)				
Z3_1400	SE5-1_cap/footing construction S5E1-01 to S5E1-04 (4nr) (N/B Stag1b + S/B Stage 0)	36	9	20-Apr-23 A	09-Nov-23	30-Dec-22	15-Feb-23	SE5-1_cap/footing construction S5E1-01 to S5E1-04 (4nr) (N/B Stag1b + S/B Stage 0)				
Z3_1410	SE5-1_backfill & remove ELS (N/B Stag1b + S/B Stage 0)	10	5	10-May-23 A	15-Nov-23	15-Feb-23	27-Feb-23	SE5-1_backfill & remove ELS (N/B Stag1b + S/B Stage 0)				
Z3_1420	SE5-2_ELS for footing/cap construction S5E2-01 to S5E2-12 (132m_2 side) (N/B Stag1b + S/B Stage 0)	37	37	08-Sep-23	25-Oct-23	07-Oct-22	19-Nov-22	SE5-2_ELS for footing/cap construction S5E2-01 to S5E2-12 (132m_2 side) (N/B Stag1b + S/B Stage 0)				
Z3_1430	SE5-2_cap/footing construction S5E2-01 to S5E2-12 (12nr) (N/B Stag1b + S/B Stage 0)	108	108	15-Sep-23	26-Jan-24	14-Oct-22	24-Feb-23	SE5-2_cap/footing construction S5E2-01 to S5E2-12 (12nr) (N/B Stag1b + S/B Stage 0)				
SOUTHBOUND												
Z3_1460	SE1-1_ELS for cap/footing construction S1E1-51P to S1E1-52 (19m_2 side) (N/B Stag1b + S/B Stage 4)	11	11	08-Sep-23	21-Sep-23	28-Dec-22	10-Jan-23	SE1-1_ELS for cap/footing construction S1E1-51P to S1E1-52 (19m_2 side) (N/B Stag1b + S/B Stage 4)				
Z3_1470	SE1-1_cap/footing construction S1E1-51P to S1E1-52 (2nr) (N/B Stag1b + S/B Stage 4)	36	36	21-Sep-23	06-Nov-23	11-Jan-23	24-Feb-23	SE1-1_cap/footing construction S1E1-51P to S1E1-52 (2nr) (N/B Stag1b + S/B Stage 4)				
Z3_1480	SE1-1_backfill & remove ELS (N/B Stag1b + S/B Stage 4)	4	4	06-Nov-23	10-Nov-23	25-Feb-23	01-Mar-23	SE1-1_backfill & remove ELS (N/B Stag1b + S/B Stage 4)				
Z3_1680	SE5-1_backfill & remove ELS	6	6	22-Sep-23	28-Sep-23	04-Jan-23	10-Jan-23	SE5-1_backfill & remove ELS				
Z3_1710	SE5-2_backfill & remove ELS	22	22	22-Sep-23	19-Oct-23	19-May-23	14-Jun-23	SE5-2_backfill & remove ELS				
SOUTHBOUND SLIP ROAD												
Z3_1740	SE8-1_ELS for footing construction SR6 1-A to SR6 4-A (34m_1 side)	10	10	13-Nov-23	23-Nov-23	12-Apr-23	24-Apr-23	SE8-1_ELS for footing construction SR6 1-A to SR6 4-A (34m_1 side)				
Z3_1750	SE8-1_footing construction SR6 1-A to SR6 4-A (4nr)	60	60	24-Nov-23	05-Feb-24	24-Apr-23	07-Jul-23	SE8-1_footing construction SR6 1-A to SR6 4-A (4nr)				
Z3_1800	SE8-1B_backfill & remove ELS	3	2	23-Jun-23 A	02-Sep-23	01-Aug-22	03-Aug-22	SE8-1B_backfill & remove ELS				
Z3_1830	SE8-2_backfill & remove ELS	1	1	23-Jun-23 A	01-Sep-23	05-Sep-22	05-Sep-22	SE8-2_backfill & remove ELS				
STRUCTURE STEEL FRAME												
NORTHBOUND SLIP ROAD												
Z3_1860	N2_SR4_erec steel posts PK1 to PK41 (41nr)	11	1	11-Jul-22 A	31-Oct-23	06-Sep-22	21-Sep-22	N2_SR4_erec steel posts PK1 to PK41				
Z3_1880	N5_RW7_erec steel posts PL1 to PL32 (32nr)	8	8	31-Oct-23	10-Nov-23	21-Sep-22	03-Oct-22	N5_RW7_erec steel posts				
ROADWORKS AND REMAINING WORKS												
ROADWORKS												
NORTHBOUND SLIP ROAD												
Z3_2700	Drainage construction MA06 to MA01 222m	139	139	31-Aug-23	19-Feb-24	21-Jul-22	05-Jan-23	Drainage construction MA06 to MA01 222m				
CENTRAL BARRIER												
Z3_2770	Drainage construction MS01 to MS08 & MS47 to MS50 319m	100	14	24-Feb-23 A	20-Sep-23	29-Nov-22	31-Mar-23	Drainage construction MS01 to MS08 & MS47 to MS50 319m				
Z3_2780	Drainage construction MN60 to MN97 220m	69	69	31-Aug-23	22-Nov-23	19-Nov-22	15-Feb-23	Drainage construction MN60 to MN97 220m				
SOUTHBOUND												
Z3_3140	Drainage construction MS56 to MS62 110m	35	0	07-Jul-23 A	21-Aug-23 A	28-Jun-23	08-Aug-23	Drainage construction MS56 to MS62 110m				
Z3_3200	Drainage construction MS72 to MS73 93m	59	59	22-Sep-23	02-Dec-23	19-May-23	29-Jul-23	Drainage construction MS72 to MS73 93m				
BRIDGE AND STRUCTURE WORKS												
PRELIMINARIES WORKS												
UTILITIES DIVERSION												
SOUTHBOUND												
Z3_3010	UU_CLP-slew 11kv cable for RW2 CH1500-1550 50m	6	6	31-Aug-23	06-Sep-23	06-Jan-23	12-Jan-23	UU_CLP-slew 11kv cable for RW2 CH1500-1550 50m				
Z3_3020	UU_NWT-slew cable for RW2 CH1525-1580 55m	13	13	07-Sep-23	21-Sep-23	13-Jan-23	31-Jan-23	UU_NWT-slew cable for RW2 CH1525-1580 55m				
Z3_3080	UU_CLP-abandoned 11kv cable for SR6 CH1850-1950 100m	19	19	31-Aug-23	21-Sep-23	10-Jun-22	02-Jul-22	UU_CLP-abandoned 11kv cable for SR6 CH1850-1950 100m				
Z3_3090	UU_HGC-slew cable for SR6 CH1800-1870 70m	8	8	13-Sep-23	21-Sep-23	23-Jun-22	02-Jul-22	UU_HGC-slew cable for SR6 CH1800-1870 70m				


 Remaining Level of Effort (Green bar), Actual Level of Effort (Black bar), Actual Work (Blue bar), Remaining Work (Light Green bar), Critical Remaining Work (Red bar), Primary Baseline (Black line), Milestone (Yellow diamond), Baseline Milestone (Black diamond)

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

3 of 6

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023							
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66			
Z3_3100	UU_HKBN-slew cable for N262 CH1800-1810 10m	1	1	31-Aug-23	31-Aug-23	31-Mar-22	31-Mar-22								
Z3_5680	UU_Construct combine UU trough between cycle track and RW1 Stage 1	75	8	08-Jun-20 A	08-Sep-23	31-Jul-20	29-Oct-20								
Z3_5685	UU_Construct combine UU trough between RW1 to SR3 Stage 2	60	6	08-Jun-20 A	06-Sep-23	02-Jun-21	13-Aug-21								
WIDENING FOR NORTH HOLLOW ABUTMENT (N264)															
Z3_4250	N264_demolish existing parapet wall	24	5	13-Oct-22 A	06-Sep-23	20-Jun-22	19-Jul-22								
Z3_4260	N264_install precast slab	18	11	28-Dec-22 A	19-Sep-23	19-Jul-22	09-Aug-22								
Z3_4270	N264_in-situ concrete slab & parapet	24	7	01-Apr-23 A	27-Sep-23	09-Aug-22	06-Sep-22								
MODIFICATION OF BRIDGE N263															
MODIFICATION EXISTING SOUTH HOLLOW ABUTMENT WALL															
Z3_3970	SHA_abutment wall construction	21	8	05-May-23 A	09-Sep-23	28-Jul-22	20-Aug-22								
DECK CONSTRUCTION OF BRIDGE N263															
Z3_3875	Construct bridge deck between SAW-1 and SHA PB-151	21	0	30-May-23 A	20-Aug-23 A	22-Aug-22	15-Sep-22								
Z3_4000	Remove existing U beam and construct bridge deck (Stage 3A/B)	100	0	14-Apr-23 A	17-Aug-23 A	10-Nov-22	14-Mar-23								
Z3_4010	Remove existing U beam and construct bridge deck (Stage 4)	70	67	22-Aug-23 A	16-Dec-23	14-Mar-23	10-Jun-23								
Z3_4020	Parapet and road road finishing works for N263	60	60	04-Nov-23	17-Jan-24	27-Apr-23	11-Jul-23								
NEW SLIP ROAD 2															
Z3_5360	SR2-1_column construction	21	12	27-Dec-21 A	12-Mar-24	15-Feb-23	11-Mar-23								
LIFT TOWER 1															
Z3_3640	Lift Tower 1_lift installation	90	77	28-Aug-23 A	01-Dec-23	27-Sep-22	16-Jan-23								
LIFT TOWER 2 & STAIRCASE															
Z3_3720	Lift Tower 2_remaining E&M works	30	3	11-Jul-23 A	02-Sep-23	17-Aug-22	22-Sep-22								
Z3_3730	Lift Tower 2_finishing works	30	6	30-Aug-23 A	06-Sep-23	17-Aug-22	22-Sep-22								
Z3_3735	Lift Tower 2_T&C	12	12	07-Sep-23	20-Sep-23	22-Sep-22	08-Oct-22								
Z3_3844	Staircase_diversion pedestrian and cyclist to new staircase	0	0		20-Sep-23		08-Oct-22								
NEW CYCLE TRACK															
Z3_4280	Demolish of existing cycle track ramp	21	21	21-Sep-23	17-Oct-23	08-Oct-22	02-Nov-22								
Z3_4290	CT-PC1_ELS & pile cap construction	21	21	18-Oct-23	11-Nov-23	14-Mar-23	12-Apr-23								
Z3_4300	CT-PC1_abutment wall construction	30	30	13-Nov-23	16-Dec-23	12-Apr-23	18-May-23								
Z3_4310	CT-PC2_ELS & footing construction	21	21	18-Oct-23	11-Nov-23	14-Mar-23	12-Apr-23								
Z3_4320	CT-PC2_column construction	21	21	13-Nov-23	06-Dec-23	12-Apr-23	08-May-23								
NEW SLIP ROAD 5															
Z3_5540	SR5-2_ELS & pile cap construction	45	0	26-Jun-23 A	08-Aug-23 A	14-Mar-23	11-May-23								
Z3_5550	SR5-2_column construction	30	14	09-Aug-23 A	14-Oct-23	11-May-23	16-Jun-23								
Z3_5560	SR5_bridge deck construction between SAW-2 and SR5-2	60	60	14-Oct-23	27-Dec-23	16-Jun-23	28-Aug-23								
Z3_5570	SR5_bridge deck construction between SR5-2 and SR5-3	60	60	18-Oct-23	29-Dec-23	16-Jun-23	28-Aug-23								
RETAINING WALL & SUBWAY															
RETAINING WALL NO.2															
Z3_4660	RW2_ELS works for Bay 201 to Bay 206 (71m_2 side)	40	40	22-Sep-23	10-Nov-23	01-Feb-23	18-Mar-23								
Z3_4670	RW2_base slab construction for Bay 201 to Bay 206	24	24	20-Oct-23	17-Nov-23	27-Feb-23	25-Mar-23								
Z3_4680	RW2_retaining wall construction for Bay 201 to Bay 206	54	54	04-Nov-23	09-Jan-24	13-Mar-23	19-May-23								
RETAINING WALL NO.3															
Z3_1218_3000	RW3_soldier pile works (13nr)	78	78	09-Sep-23	13-Dec-23	22-Aug-22	23-Nov-22								
RETAINING WALL NO.5															
Z3_4880	RW5 Combined SE4_ELS works for Bay500 to 505 (48m_2 side)	27	9	08-Jun-23 A	30-Oct-23	14-Jan-23	18-Feb-23								
Z3_4890	RW5 Combined SE4_base slab construction for Bay 500 to 505	60	21	07-Jul-23 A	11-Nov-23	03-Feb-23	19-Apr-23								
MODIFY EXISTING RETAINING WALL SR6															
Z3_5190	SR6_remove ELS & backfill for Bay SR601 to SR609	8	3	23-Jun-23 A	25-Sep-23	26-Nov-22	05-Dec-22								
WORK BETWEEN FOOTBRIDGE NF40 AND NF66 (ZONE 4)															
PRELIMINARIES WORKS															
SUMMARY PROGRAMME															
Z4SU1005	Zone 4 Stage 1 NB & SB foundation/stem wall	434	81	06-Mar-20 A	06-Dec-23	31-Mar-20	16-Sep-21								
Z4SU1100	Zone 4 NF66 Construction	220	0	20-Jul-20 A	14-Mar-23 A	31-Aug-20	31-May-21								
UTILITIES DIVERSION															

█ Remaining Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Level of Effort
 █ Critical Remaining Work
 ◆ Baseline Milesto...
█ Actual Work
 █ Primary Baseline

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

4 of 6

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023					
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66	
NORTHBOUND													
Z4_1280	UU_CATV-slew cable for N4 CH2190-2400 210m	25	25	31-Aug-23	28-Sep-23	05-Aug-22	02-Sep-22						
SOUTHBOUND													
Z4_1380	UU_Salt watermain for SE6 CH2275-2345 56m 700mm	20	20	31-Aug-23	23-Sep-23	11-Apr-22	09-May-22						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE CAP AND FOOTING													
NORTHBOUND													
Z4_1000	N4_ELS for pile cap construction N4-12P to N4-27P (231m_2 side)	64	9	20-May-23 A	11-Oct-23	03-Sep-22	19-Nov-22						
Z4_1010	N4_pile cap/stem wall construction N4-12P to N4-27P (15nr)	90	12	29-Jun-23 A	14-Oct-23	14-Oct-22	02-Feb-23						
Z4_1020	N4_backfill & remove ELS	39	39	21-Oct-23	06-Dec-23	07-Jan-23	24-Feb-23						
CENTRAL BARRIER													
Z4_1070	SE6_ELS for footing/cap construction S6E1-01A to S6E1-10 (165m_2 side)	42	0	30-Jun-23 A	03-Aug-23 A	25-Feb-23	19-Apr-23						
Z4_1081	SE6_Re-align TTA for central median footing S6E1-11 to S6E1-16	24	24	11-Sep-23	11-Oct-23	06-Sep-22	06-Oct-22						
Z4_1082	SE6_ELS for footing/cap construction S6E1-11 to S6E1-16 (67m_2 side)	34	17	01-Aug-23 A	01-Nov-23	07-Oct-22	15-Nov-22						
Z4_1084	SE6_cap/footing/stem wall construction S6E1-11 to S6E1-16 (6nr)	108	81	05-Aug-23 A	18-Jan-24	27-Oct-22	08-Mar-23						
STRUCTURE STEEL FRAME													
SOUTHBOUND													
Z4_1180	SE6_erect steel posts PV1 to PV59 (59nr)	15	2	31-Aug-22 A	02-Sep-23	09-Jun-22	27-Jun-22						
ROADWORKS AND REMAINING WORKS													
ROADWORKS													
NORTHBOUND													
Z4_1220	Drainage construction MN145 to MN148 180m	30	30	02-Nov-23	06-Dec-23	18-Jan-23	24-Feb-23						
SOUTHBOUND													
Z4_1250	Drainage construction MS83 to MS87 279m	47	9	15-Jun-22 A	11-Sep-23	05-May-22	30-Jun-22						
WORK BETWEEN FOOTBRIDGE NF66 AND FO TAN ROAD (ZONE 5)													
PRELIMINARIES WORKS													
SUMMARY PROGRAMME													
Z5SU1005	Zone 5 Stage 1 NB & SB foundation/stem wall	467	74	10-Feb-20 A	28-Nov-23	31-Mar-20	28-Oct-21						
UTILITIES DIVERSION													
SOUTHBOUND													
Z5_1860	UU_Salt watermain for SE3 CH2360-2530 179m 700mm	60	60	23-Sep-23	06-Dec-23	09-May-22	20-Jul-22						
NOISE BARRIER AND SEMI-ENCLOSURE													
PILE CAP AND FOOTING													
NORTHBOUND													
Z5_1020	N4_ELS for footing/cap construction N4-29P to N4-51 (322m_2 side)	161	24	01-Feb-21 A	28-Sep-23	11-May-21	20-Nov-21						
Z5_1030	N4_cap/footing/stem wall construction N4-29 to N4-51 (23nr)	216	47	27-Mar-21 A	27-Oct-23	25-May-21	12-Feb-22						
Z5_1050	N4_backfill & remove ELS	54	12	14-Apr-21 A	28-Nov-23	28-Oct-22	03-Jan-23						
CENTRAL BARRIER													
Z5_1100	SE3-1_ELS for footing/cap construction S3E1-01 to S3E1-22p (305m_2 side)	84	65	18-May-23 A	22-Dec-23	24-Aug-22	02-Dec-22						
SOUTHBOUND													
Z5_1190	SE3-1_ELS for footing/cap construction S3E1-51P to S3E1-74P (313m_2 side)	58	3	03-Jan-22 A	02-Sep-23	29-Apr-22	09-Jul-22						
Z5_1200	SE3-1_footing/stem wall construction S3E1-51P to S3E1-74P & N3-01 (21nr)	198	10	21-Jan-22 A	11-Sep-23	26-Mar-22	24-Nov-22						
Z5_1220	SE3-1_backfill & remove ELS	52	47	15-Sep-22 A	27-Oct-23	23-Sep-22	25-Nov-22						
Z5_1222	SE3-2_ELS for footing construction S3E2-51 to S3E2-53 (32m_2 side)	16	16	31-Aug-23	18-Sep-23	10-Jun-22	29-Jun-22						
Z5_1224	SE3-2_footing/cap/stem wall construction S3E2-51 to 53 (2nr)	36	36	19-Sep-23	02-Nov-23	29-Jun-22	11-Aug-22						
Z5_1226	SE3-2_backfill & remove ELS	22	22	03-Nov-23	28-Nov-23	11-Aug-22	06-Sep-22						
STRUCTURE STEEL FRAME													
NORTHBOUND													
Z5_1060	N4_erect steel posts PK199 to PK268 (81nr)	21	21	28-Nov-23	29-Dec-23	03-Jan-23	06-Feb-23						
SOUTHBOUND													
Z5_1430	SE3-2_erect steel posts PY79 to PY112 (34nr)	9	9	06-Oct-23	19-Oct-23	07-Jun-22	17-Jun-22						
SOUTHBOUND SLIP ROAD													
Z5_1450	N3_erect steel posts PW1 to PW7 (7nr)	2	1	07-Jul-22 A	01-Sep-23	10-Jun-22	14-Jun-22						
NOISE BARRIER PANEL													

■ Remaining Level of Effort
 ■ Remaining Work
 ■ Actual Work
■ Actual Level of Effort
 ■ Critical Remaining Work
 ■ Primary Baseline
■ Actual Work
 ■ Primary Baseline











◆ Milestone
 ◆ Baseline Milesto...

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

5 of 6

Activity ID	Activity Name	Original Duration	Remaining Duration	3MRP Start	3MRP Finish	AP13 Start	AP13 Finish	2023					
								Aug 62	Sep 63	Oct 64	Nov 65	Dec 66	
SOUTHBOUND SLIP ROAD													
Z5_1470	N3_install noise barrier wall panel PW1 to PW7 (96 sq.m)	1	1	07-Oct-22 A	04-Sep-23	29-Jun-22	30-Jun-22						
Z5_1480	R4_install noise barrier wall panel PW8 to PW48 (651 sq.m)	4	1	07-Oct-22 A	05-Sep-23	17-Aug-22	23-Aug-22						
ROADWORKS AND REMAINING WORKS													
ROADWORKS													
NORTHBOUND													
Z5_1490	Drainage construction MN170 to MN172 129m	40	40	03-Oct-23	20-Nov-23	05-Nov-22	22-Dec-22						
SOUTHBOUND													
Z5_1550	Drainage construction MS109 to MS112 & MS123 to MS124 246m	77	15	01-Sep-22 A	18-Oct-23	16-Aug-22	17-Nov-22						
Z5_1560	Drainage construction MS126 to MS128 144m	45	23	04-Jul-22 A	26-Sep-23	31-Mar-22	27-May-22						
SOUTHBOUND SLIP ROAD													
Z5_1600	Zone 5_road surfacing with flexible pavement Type 2 1257m2	9	9	05-Sep-23	18-Sep-23	23-Aug-22	05-Sep-22						
GEOTECHNICAL WORKS													
NORTHBOUND SLIP ROAD													
Z5_1820	Zone 5_fill replacement 7SE-A/F164 (compacted fill)	53	49	20-Mar-23 A	07-Nov-23	27-Sep-22	30-Nov-22						
SOUTHBOUND SLIP ROAD													
Z5_1740	Zone 5_fill replacement by no-fines concrete 7SE-A/F166 (open excavation)	29	3	12-Mar-21 A	02-Sep-23	07-Apr-22	14-May-22						
Z5_1810	Zone 5_fill replacement 7SE-A/F165 (compacted fill)	20	4	02-Mar-23 A	07-Sep-23	06-Aug-22	30-Aug-22						

 Remaining Level of Effort	 Remaining Work	 Milestone	 Milestone
 Actual Level of Effort	 Critical Remaining Work	 Baseline Milesto...	 Baseline Milesto...
 Actual Work	 Primary Baseline		

Contract No. NE/2017/05
Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin)
3 Months Rolling Programme (31/08/23)

Date	Revision	Checked	Approved
08-Sep-23	3MRP DWP 2308	EGA	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com




Appendix B

Project Organization Chart

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com

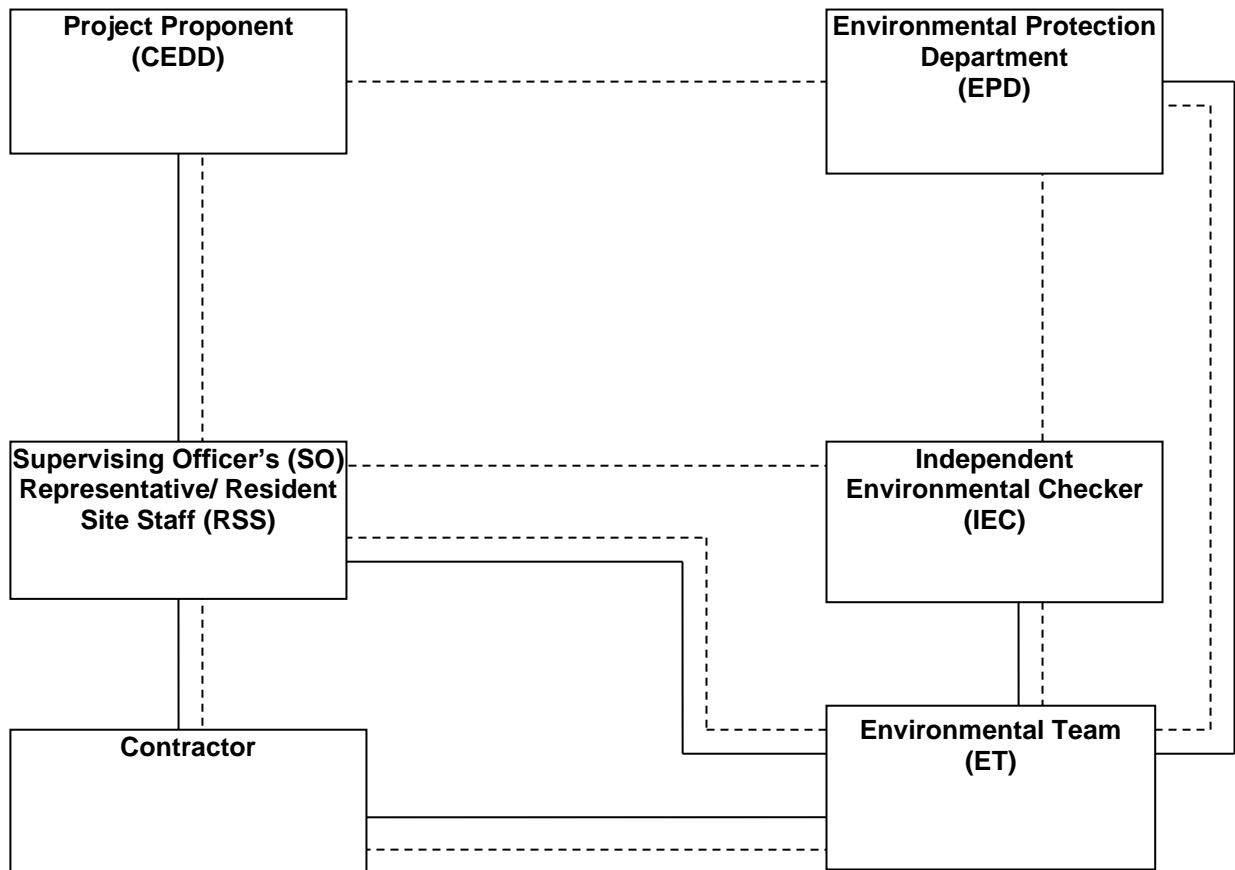

Legend:
—— Line of Reporting
- - - - Line of Communication

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix C

Action and Limit Levels for Air Quality and Noise

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Action and Limit Levels for 24-hr TSP and 1-hr TSP

Parameter	Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
24-hr TSP ($\mu\text{g}/\text{m}^3$)	AMS1	171	260
	AMS2	166	
	AMS3A	200	
	AMS4A	200	
	AMS5	156	
	AMS6	165	
	AMS7A	171	
	AMS8	161	
	AMS9	159	
	AMS10	155	
	AMS11A	165	
	AMS12	168	
	AMS13	174	
	AMS14	174	
	AMS15	172	
	AMS16	180	
	AMS17	171	
	AMS18	175	
	AMS19	174	
1-hr TSP ($\mu\text{g}/\text{m}^3$)	AMS1	350	500
	AMS2	324	
	AMS3A	350	
	AMS4A	348	
	AMS5	340	
	AMS6	347	
	AMS7A	344	
	AMS8	336	
	AMS9	327	
	AMS10	330	
	AMS11A	335	
	AMS12	296	
	AMS13	303	
	AMS14	350	
	AMS15	350	
	AMS16	310	
	AMS17	338	
	AMS18	308	
	AMS19	305	

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Action and Limit Levels for Construction Noise, Leq (30min), dB(A)

Time Period	Location	Action	Limit
0700-1900 hrs on normal weekdays	NMS1 NMS2 NMS3 NMS4 NMS5A NMS6A NMS7 NMS8 NMS9 NMS10A* NMS11 NMS12* NMS13 NMS14 NMS15 NMS16 NMS17* NMS18 NMS19 NMS20 NMS23 NMS24 NMS25A NMS26 NMS27*	When one documented complaint is received	75 dB(A)

* For NMS 10A, 12, 17 and 27, the Limit Level is reduced to 70 dB(A) for schools and 65 dB(A) during school examination periods.

Action and Limit Levels for Construction Noise, Leq (15min), dB(A)

Time Period	Location	Action	Limit
2300-0700 hrs of next day	NMS1 NMS2 NMS3 NMS4 NMS5A NMS6A NMS7 NMS8 NMS9 NMS11 NMS13 NMS14 NMS15 NMS16 NMS18 NMS19 NMS20 NMS23 NMS24 NMS25A NMS26	When one documented complaint is received	55 dB(A)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix D

Graphical Presentation of Monitoring Data

**1-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 4A - Wai Wah Centre (Site Boundary)

1-hour TSP ($\mu\text{g}/\text{m}^3$)										
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather		
04-May-23	17:44	49	46	49	48	348	500	Fine		
10-May-23	14:09	56	55	59	57			Fine		
16-May-23	07:49	46	49	44	46			Fine		
23-May-23	03:10	69	69	69	69			Fine		
27-May-23	11:22	86	84	80	83			Fine		
01-Jun-23	10:40	44	44	44	44			Fine		
07-Jun-23	10:26	68	73	66	69			Fine		
13-Jun-23	08:00	68	66	66	67			Fine		
19-Jun-23	13:56	41	47	43	44			Fine		
29-Jun-23	08:52	41	37	45	41			Fine		
05-Jul-23	10:55	40	45	48	44			Fine		
11-Jul-23	15:58	45	41	43	43			Fine		
18-Jul-23	11:10	30	32	30	31			Overcast		
22-Jul-23	14:12	58	56	53	56			Fine		
29-Jul-23	10:59	37	37	39	38			Fine		
03-Aug-23	09:14	28	24	26	26			Overcast		
09-Aug-23	07:46	32	27	29	29			Fine		
15-Aug-23	08:30	32	34	34	33			Fine		
21-Aug-23	13:13	34	32	32	33			Cloudy		
26-Aug-23	10:41	52	54	54	53			Fine		
Average					48					
Max					86					
Min					24					

AMS7A - Sheung Wo Che

1-hour TSP ($\mu\text{g}/\text{m}^3$)										
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather		
04-May-23	15:56	53	49	52	51	344	500	Fine		
10-May-23	15:19	52	53	52	52			Fine		
16-May-23	10:01	53	52	50	52			Fine		
22-May-23	11:19	53	50	50	51			Fine		
27-May-23	07:30	66	72	70	69			Fine		
01-Jun-23	14:18	48	46	50	48			Fine		
07-Jun-23	14:44	70	76	66	71			Fine		
13-Jun-23	13:49	58	56	60	58			Fine		
19-Jun-23	09:05	48	46	48	47			Fine		
29-Jun-23	17:01	40	44	44	43			Fine		
05-Jul-23	10:05	48	48	50	49			Fine		
11-Jul-23	12:07	48	40	48	45			Fine		
18-Jul-23	12:56	32	28	32	31			Fine		
22-Jul-23	14:24	56	60	52	56			Fine		
29-Jul-23	14:08	42	44	46	44			Fine		
03-Aug-23	10:01	28	22	26	25			Fine		
09-Aug-23	16:31	30	32	32	31			Fine		
15-Aug-23	08:04	30	28	30	29			Fine		
21-Aug-23	08:58	30	32	32	31			Cloudy		
26-Aug-23	13:11	50	59	50	53			Fine		
Average					47					
Max					76					
Min					22					

AMS 12 - Fung Wo Estate


1-hour TSP ($\mu\text{g}/\text{m}^3$)										
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather		
04-May-23	11:05	47	48	43	46	296	500	Fine		
10-May-23	16:30	36	38	39	38			Fine		
16-May-23	15:11	44	40	47	44			Fine		
23-May-23	01:32	41	35	38	38			Fine		
27-May-23	12:48	72	72	80	75			Fine		
01-Jun-23	09:04	45	41	49	45			Fine		
07-Jun-23	09:12	76	69	74	73			Fine		
13-Jun-23	12:40	59	63	63	62			Fine		
19-Jun-23	10:14	45	49	51	48			Fine		
29-Jun-23	8:10	59	49	47	52			Fine		
05-Jul-23	10:15	51	57	49	52			Fine		
11-Jul-23	08:16	51	55	43	50			Fine		
18-Jul-23	14:44	34	34	34	34			Overcast		
22-Jul-23	16:31	61	65	63	63			Fine		
29-Jul-23	12:17	49	47	47	48			Fine		
03-Aug-23	12:46	30	30	28	29			Overcast		
09-Aug-23	8:14	34	34	30	33			Fine		
15-Aug-23	13:40	32	30	28	30			Fine		
21-Aug-23	14:46	32	34	34	33			Cloudy		
26-Aug-23	12:34	36	30	27	31			Fine		
Average			46							
Max			80							
Min			27							

AMS 17 - Wo Che Estate


1-hour TSP ($\mu\text{g}/\text{m}^3$)										
Date	Start Time	1st hr	2nd hr	3rd hr	Average	Action Level	Limit Level	Weather		
04-May-23	13:14	46	41	47	45	338	500	Fine		
10-May-23	11:49	48	48	49	48			Fine		
16-May-23	13:19	46	50	44	47			Fine		
23-May-23	02:50	52	50	50	51			Fine		
27-May-23	17:22	79	90	98	89			Fine		
01-Jun-23	11:52	49	49	47	48			Fine		
08-Jun-23	01:23	61	69	63	64			Fine		
13-Jun-23	09:30	63	61	59	61			Fine		
19-Jun-23	11:22	51	49	47	49			Fine		
29-Jun-23	13:18	51	43	47	47			Fine		
05-Jul-23	8:23	47	49	53	50			Fine		
11-Jul-23	13:24	47	49	45	47			Fine		
18-Jul-23	12:31	31	33	33	32			Fine		
22-Jul-23	17:43	61	63	69	64			Fine		
29-Jul-23	11:25	41	47	49	46			Fine		
04-Aug-23	2:32	27	29	27	28			Fine		
09-Aug-23	15:02	34	34	32	33			Fine		
15-Aug-23	07:52	33	29	33	32			Fine		
21-Aug-23	13:32	34	32	30	32			Cloudy		
26-Aug-23	16:58	36	24	28	29			Fine		
Average			47							
Max			98							
Min			24							

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.


1-hr TSP Monitoring record for AMS4

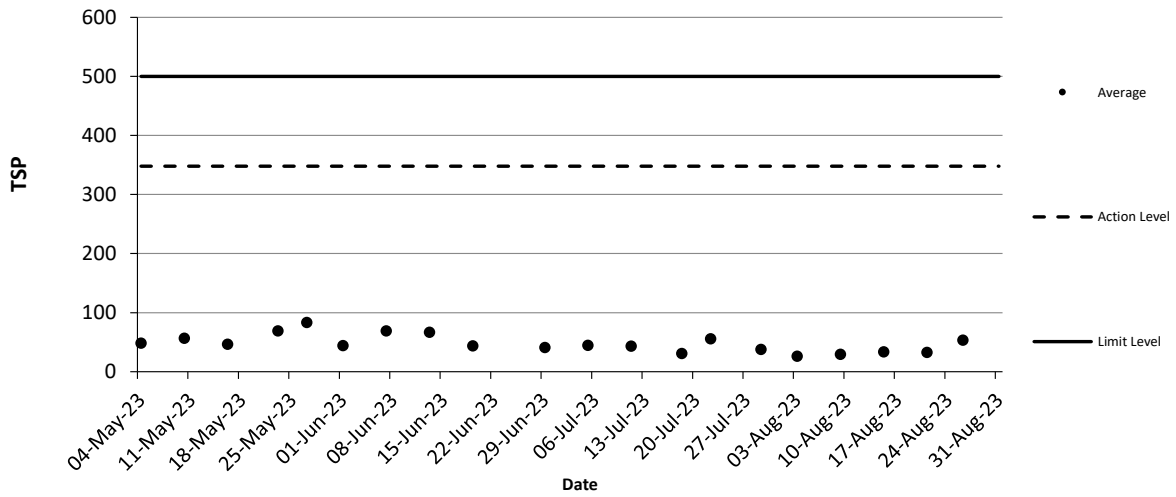


1-hr TSP Monitoring record for AMS7A

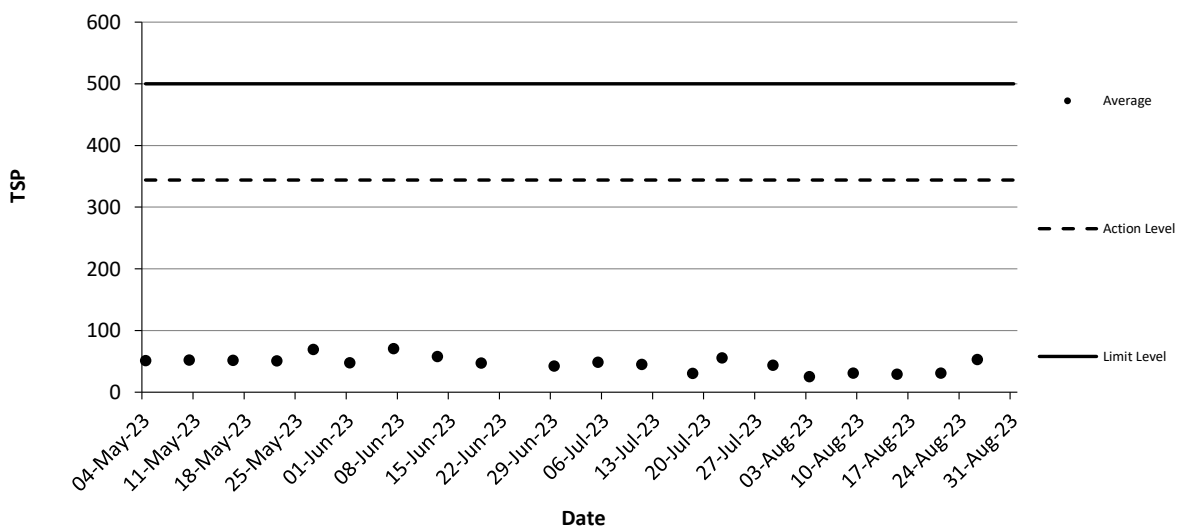

1-hr TSP Monitoring record for AMS12

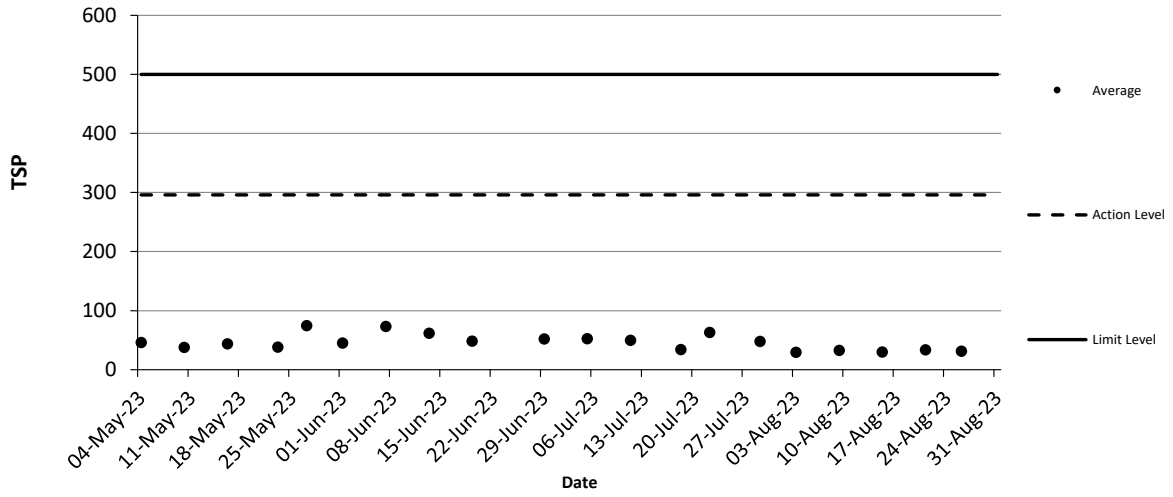

1-hr TSP Monitoring record for AMS17

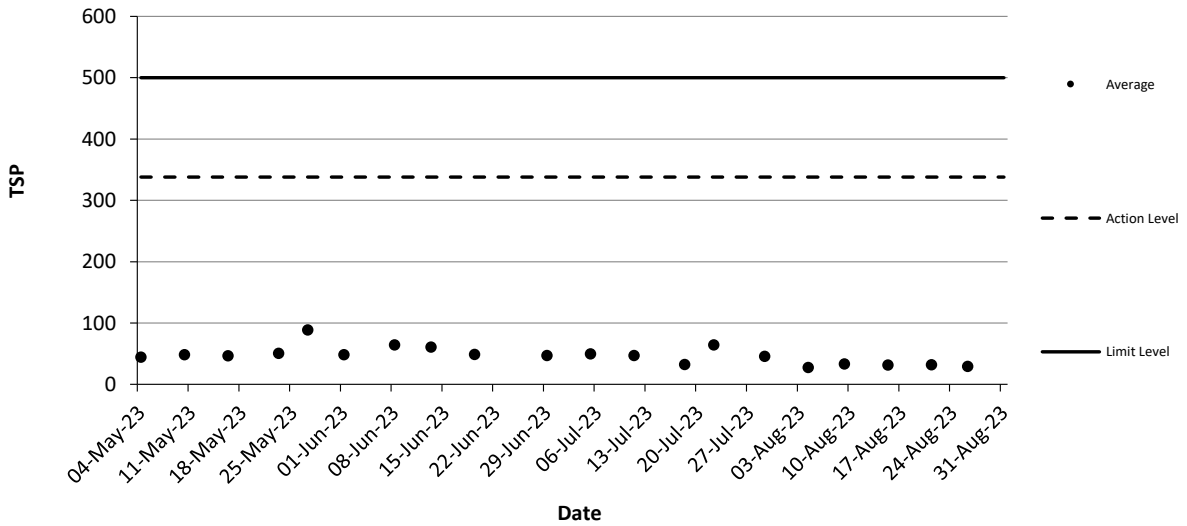

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 4A - Wai Wah Centre (Site Boundary)

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
04-05-23 07:44	44
04-05-23 08:44	47
04-05-23 09:44	42
04-05-23 10:44	43
04-05-23 11:44	42
04-05-23 12:44	43
04-05-23 13:44	43
04-05-23 14:44	46
04-05-23 15:44	44
04-05-23 16:44	47
04-05-23 17:44	49
04-05-23 18:44	46
04-05-23 19:44	49
04-05-23 20:44	43
04-05-23 21:44	42
04-05-23 22:44	46
04-05-23 23:44	39
05-05-23 00:44	39
05-05-23 01:44	37
05-05-23 02:44	42
05-05-23 03:44	43
05-05-23 04:44	42
05-05-23 05:44	39
05-05-23 06:44	40
Average	43
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
10-05-23 07:09	53
10-05-23 08:09	55
10-05-23 09:09	56
10-05-23 10:09	56
10-05-23 11:09	57
10-05-23 12:09	56
10-05-23 13:09	57
10-05-23 14:09	56
10-05-23 15:09	55
10-05-23 16:09	59
10-05-23 17:09	56
10-05-23 18:09	55
10-05-23 19:09	53
10-05-23 20:09	55
10-05-23 21:09	56
10-05-23 22:09	55
10-05-23 23:09	57
11-05-23 00:09	53
11-05-23 01:09	55
11-05-23 02:09	56
11-05-23 03:09	53
11-05-23 04:09	55
11-05-23 05:09	52
11-05-23 06:09	53
Average	55
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16-05-23 07:49	46
16-05-23 08:49	49
16-05-23 09:49	44
16-05-23 10:49	44
16-05-23 11:49	46
16-05-23 12:49	47
16-05-23 13:49	43
16-05-23 14:49	42
16-05-23 15:49	46
16-05-23 16:49	42
16-05-23 17:49	43
16-05-23 18:49	42
16-05-23 19:49	40
16-05-23 20:49	40
16-05-23 21:49	37
16-05-23 22:49	40
16-05-23 23:49	39
17-05-23 00:49	42
17-05-23 01:49	36
17-05-23 02:49	39
17-05-23 03:49	40
17-05-23 04:49	42
17-05-23 05:49	44
17-05-23 06:49	47
Average	43
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22-05-23 07:10	57
22-05-23 08:10	60
22-05-23 09:10	57
22-05-23 10:10	60
22-05-23 11:10	59
22-05-23 12:10	59
22-05-23 13:10	60
22-05-23 14:10	59
22-05-23 15:10	59
22-05-23 16:10	60
22-05-23 17:10	62
22-05-23 18:10	59
22-05-23 19:10	63
22-05-23 20:10	60
22-05-23 21:10	60
22-05-23 22:10	60
22-05-23 23:10	56
23-05-23 00:10	59
23-05-23 01:10	57
23-05-23 02:10	67
23-05-23 03:10	69
23-05-23 04:10	69
23-05-23 05:10	69
23-05-23 06:10	67
Average	61
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
27-05-23 07:22	57
27-05-23 08:22	63
27-05-23 09:22	71
27-05-23 10:22	69
27-05-23 11:22	86
27-05-23 12:22	84
27-05-23 13:22	80
27-05-23 14:22	73
27-05-23 15:22	73
27-05-23 16:22	67
27-05-23 17:22	61
27-05-23 18:22	73
27-05-23 19:22	76
27-05-23 20:22	80
27-05-23 21:22	78
27-05-23 22:22	74
27-05-23 23:22	71
28-05-23 00:22	55
28-05-23 01:22	57
28-05-23 02:22	59
28-05-23 03:22	63
28-05-23 04:22	61
28-05-23 05:22	67
28-05-23 06:22	63
Average	69
Action Level	200
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 4A - Wai Wah Centre (Site Boundary)

Date and Time	TSP Concentration (µg/m³)
01-06-23 07:40	44
01-06-23 08:40	42
01-06-23 09:40	38
01-06-23 10:40	44
01-06-23 11:40	44
01-06-23 12:40	44
01-06-23 13:40	40
01-06-23 14:40	42
01-06-23 15:40	42
01-06-23 16:40	45
01-06-23 17:40	42
01-06-23 18:40	40
01-06-23 19:40	36
01-06-23 20:40	36
01-06-23 21:40	38
01-06-23 22:40	34
01-06-23 23:40	38
02-06-23 00:40	40
02-06-23 01:40	36
02-06-23 02:40	40
02-06-23 03:40	44
02-06-23 04:40	44
02-06-23 05:40	40
02-06-23 06:40	42
Average	41
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
07-06-23 07:26	56
07-06-23 08:26	60
07-06-23 09:26	62
07-06-23 10:26	68
07-06-23 11:26	73
07-06-23 12:26	66
07-06-23 13:26	58
07-06-23 14:26	60
07-06-23 15:26	56
07-06-23 16:26	58
07-06-23 17:26	54
07-06-23 18:26	51
07-06-23 19:26	49
07-06-23 20:26	53
07-06-23 21:26	66
07-06-23 22:26	45
07-06-23 23:26	51
08-06-23 00:26	54
08-06-23 01:26	43
08-06-23 02:26	64
08-06-23 03:26	66
08-06-23 04:26	71
08-06-23 05:26	43
08-06-23 06:26	54
Average	58
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
13-06-23 08:00	68
13-06-23 09:00	66
13-06-23 10:00	66
13-06-23 11:00	62
13-06-23 12:00	64
13-06-23 13:00	66
13-06-23 14:00	60
13-06-23 15:00	60
13-06-23 16:00	62
13-06-23 17:00	64
13-06-23 18:00	66
13-06-23 19:00	62
13-06-23 20:00	56
13-06-23 21:00	58
13-06-23 22:00	60
13-06-23 23:00	60
14-06-23 00:00	56
14-06-23 01:00	60
14-06-23 02:00	60
14-06-23 03:00	58
14-06-23 04:00	62
14-06-23 05:00	64
14-06-23 06:00	68
14-06-23 07:00	66
Average	62
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
19-06-23 07:56	34
19-06-23 08:56	35
19-06-23 09:56	41
19-06-23 10:56	37
19-06-23 11:56	32
19-06-23 12:56	39
19-06-23 13:56	41
19-06-23 14:56	47
19-06-23 15:56	43
19-06-23 16:56	37
19-06-23 17:56	39
19-06-23 18:56	41
19-06-23 19:56	37
19-06-23 20:56	34
19-06-23 21:56	32
19-06-23 22:56	32
19-06-23 23:56	35
20-06-23 00:56	32
20-06-23 01:56	30
20-06-23 02:56	35
20-06-23 03:56	37
20-06-23 04:56	39
20-06-23 05:56	34
20-06-23 06:56	34
Average	37
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
29-06-23 07:52	35
29-06-23 08:52	41
29-06-23 09:52	37
29-06-23 10:52	45
29-06-23 11:52	34
29-06-23 12:52	28
29-06-23 13:52	30
29-06-23 14:52	30
29-06-23 15:52	35
29-06-23 16:52	39
29-06-23 17:52	32
29-06-23 18:52	41
29-06-23 19:52	34
29-06-23 20:52	30
29-06-23 21:52	30
29-06-23 22:52	28
29-06-23 23:52	35
30-06-23 00:52	37
30-06-23 01:52	28
30-06-23 02:52	28
30-06-23 03:52	34
30-06-23 04:52	30
30-06-23 05:52	32
30-06-23 06:52	35
Average	34
Action Level	200
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 4A - Wai Wah Centre (Site Boundary)

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
05-07-23 07:55	38
05-07-23 08:55	42
05-07-23 09:55	40
05-07-23 10:55	40
05-07-23 11:55	45
05-07-23 12:55	48
05-07-23 13:55	40
05-07-23 14:55	42
05-07-23 15:55	40
05-07-23 16:55	37
05-07-23 17:55	44
05-07-23 18:55	44
05-07-23 19:55	38
05-07-23 20:55	40
05-07-23 21:55	34
05-07-23 22:55	34
05-07-23 23:55	30
06-07-23 00:55	36
06-07-23 01:55	38
06-07-23 02:55	38
06-07-23 03:55	42
06-07-23 04:55	40
06-07-23 05:55	36
06-07-23 06:55	34
Average	39
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
11-07-23 07:58	41
11-07-23 08:58	37
11-07-23 09:58	37
11-07-23 10:58	37
11-07-23 11:58	39
11-07-23 12:58	43
11-07-23 13:58	39
11-07-23 14:58	37
11-07-23 15:58	45
11-07-23 16:58	41
11-07-23 17:58	43
11-07-23 18:58	37
11-07-23 19:58	34
11-07-23 20:58	35
11-07-23 21:58	35
11-07-23 22:58	39
11-07-23 23:58	34
12-07-23 00:58	35
12-07-23 01:58	41
12-07-23 02:58	39
12-07-23 03:58	37
12-07-23 04:58	41
12-07-23 05:58	41
12-07-23 06:58	43
Average	39
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
18-07-23 08:10	28
18-07-23 09:10	26
18-07-23 10:10	26
18-07-23 11:10	30
18-07-23 12:10	32
18-07-23 13:10	30
18-07-23 14:10	28
18-07-23 15:10	28
18-07-23 16:10	30
18-07-23 17:10	26
18-07-23 18:10	22
18-07-23 19:10	26
18-07-23 20:10	22
18-07-23 21:10	24
18-07-23 22:10	22
18-07-23 23:10	22
19-07-23 00:10	26
19-07-23 01:10	22
19-07-23 02:10	20
19-07-23 03:10	20
19-07-23 04:10	24
19-07-23 05:10	24
19-07-23 06:10	26
19-07-23 07:10	24
Average	25
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22-07-23 08:12	47
22-07-23 09:12	45
22-07-23 10:12	43
22-07-23 11:12	49
22-07-23 12:12	41
22-07-23 13:12	51
22-07-23 14:12	58
22-07-23 15:12	56
22-07-23 16:12	53
22-07-23 17:12	49
22-07-23 18:12	45
22-07-23 19:12	41
22-07-23 20:12	43
22-07-23 21:12	39
22-07-23 22:12	37
22-07-23 23:12	37
23-07-23 00:12	45
23-07-23 01:12	49
23-07-23 02:12	39
23-07-23 03:12	45
23-07-23 04:12	53
23-07-23 05:12	51
23-07-23 06:12	49
23-07-23 07:12	56
Average	47
Action Level	200
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
29-07-23 07:59	34
29-07-23 08:59	41
29-07-23 09:59	35
29-07-23 10:59	37
29-07-23 11:59	37
29-07-23 12:59	39
29-07-23 13:59	34
29-07-23 14:59	32
29-07-23 15:59	35
29-07-23 16:59	37
29-07-23 17:59	39
29-07-23 18:59	37
29-07-23 19:59	34
29-07-23 20:59	30
29-07-23 21:59	32
29-07-23 22:59	30
29-07-23 23:59	35
30-07-23 00:59	34
30-07-23 01:59	30
30-07-23 02:59	30
30-07-23 03:59	34
30-07-23 04:59	37
30-07-23 05:59	39
30-07-23 06:59	37
Average	35
Action Level	200
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 4A - Wai Wah Centre (Site Boundary)

Date and Time	TSP Concentration (µg/m³)
03-08-23 08:14	22
03-08-23 09:14	28
03-08-23 10:14	24
03-08-23 11:14	26
03-08-23 12:14	24
03-08-23 13:14	22
03-08-23 14:14	22
03-08-23 15:14	20
03-08-23 16:14	20
03-08-23 17:14	18
03-08-23 18:14	20
03-08-23 19:14	24
03-08-23 20:14	24
03-08-23 21:14	18
03-08-23 22:14	17
03-08-23 23:14	17
04-08-23 00:14	18
04-08-23 01:14	17
04-08-23 02:14	20
04-08-23 03:14	20
04-08-23 04:14	22
04-08-23 05:14	24
04-08-23 06:14	22
04-08-23 07:14	18
Average	21
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
09-08-23 07:46	32
09-08-23 08:46	27
09-08-23 09:46	29
09-08-23 10:46	29
09-08-23 11:46	29
09-08-23 12:46	27
09-08-23 13:46	30
09-08-23 14:46	25
09-08-23 15:46	25
09-08-23 16:46	29
09-08-23 17:46	27
09-08-23 18:46	23
09-08-23 19:46	23
09-08-23 20:46	23
09-08-23 21:46	25
09-08-23 22:46	27
09-08-23 23:46	25
10-08-23 00:46	21
10-08-23 01:46	21
10-08-23 02:46	25
10-08-23 03:46	23
10-08-23 04:46	23
10-08-23 05:46	21
10-08-23 06:46	25
Average	26
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
15-08-23 08:30	32
15-08-23 09:30	34
15-08-23 10:30	34
15-08-23 11:30	32
15-08-23 12:30	32
15-08-23 13:30	32
15-08-23 14:30	30
15-08-23 15:30	30
15-08-23 16:30	30
15-08-23 17:30	28
15-08-23 18:30	24
15-08-23 19:30	24
15-08-23 20:30	26
15-08-23 21:30	26
15-08-23 22:30	26
15-08-23 23:30	24
16-08-23 00:30	22
16-08-23 01:30	22
16-08-23 02:30	26
16-08-23 03:30	26
16-08-23 04:30	24
16-08-23 05:30	22
16-08-23 06:30	28
16-08-23 07:30	26
Average	28
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
21-08-23 08:13	28
21-08-23 09:13	28
21-08-23 10:13	30
21-08-23 11:13	30
21-08-23 12:13	30
21-08-23 13:13	34
21-08-23 14:13	32
21-08-23 15:13	32
21-08-23 16:13	30
21-08-23 17:13	28
21-08-23 18:13	28
21-08-23 19:13	28
21-08-23 20:13	26
21-08-23 21:13	28
21-08-23 22:13	24
21-08-23 23:13	24
22-08-23 00:13	26
22-08-23 01:13	26
22-08-23 02:13	22
22-08-23 03:13	22
22-08-23 04:13	24
22-08-23 05:13	26
22-08-23 06:13	28
22-08-23 07:13	26
Average	28
Action Level	200
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
26-08-23 08:41	44
26-08-23 09:41	39
26-08-23 10:41	52
26-08-23 11:41	54
26-08-23 12:41	54
26-08-23 13:41	50
26-08-23 14:41	48
26-08-23 15:41	46
26-08-23 16:41	33
26-08-23 17:41	37
26-08-23 18:41	29
26-08-23 19:41	29
26-08-23 20:41	48
26-08-23 21:41	46
26-08-23 22:41	50
26-08-23 23:41	37
27-08-23 00:41	35
27-08-23 01:41	41
27-08-23 02:41	44
27-08-23 03:41	50
27-08-23 04:41	48
27-08-23 05:41	41
27-08-23 06:41	39
27-08-23 07:41	37
Average	43
Action Level	200
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS7A - Sheung Wo Che

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
04-05-23 07:56	50
04-05-23 08:56	52
04-05-23 09:56	47
04-05-23 10:56	49
04-05-23 11:56	52
04-05-23 12:56	46
04-05-23 13:56	44
04-05-23 14:56	50
04-05-23 15:56	53
04-05-23 16:56	49
04-05-23 17:56	52
04-05-23 18:56	47
04-05-23 19:56	44
04-05-23 20:56	47
04-05-23 21:56	41
04-05-23 22:56	41
04-05-23 23:56	43
05-05-23 00:56	46
05-05-23 01:56	40
05-05-23 02:56	41
05-05-23 03:56	44
05-05-23 04:56	47
05-05-23 05:56	46
05-05-23 06:56	46
Average	47
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
10-05-23 07:19	48
10-05-23 08:19	46
10-05-23 09:19	48
10-05-23 10:19	50
10-05-23 11:19	49
10-05-23 12:19	48
10-05-23 13:19	49
10-05-23 14:19	50
10-05-23 15:19	52
10-05-23 16:19	53
10-05-23 17:19	52
10-05-23 18:19	50
10-05-23 19:19	50
10-05-23 20:19	49
10-05-23 21:19	52
10-05-23 22:19	49
10-05-23 23:19	48
11-05-23 00:19	46
11-05-23 01:19	49
11-05-23 02:19	50
11-05-23 03:19	45
11-05-23 04:19	46
11-05-23 05:19	49
11-05-23 06:19	45
Average	49
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16-05-23 08:01	50
16-05-23 09:01	50
16-05-23 10:01	53
16-05-23 11:01	52
16-05-23 12:01	50
16-05-23 13:01	49
16-05-23 14:01	46
16-05-23 15:01	52
16-05-23 16:01	49
16-05-23 17:01	47
16-05-23 18:01	47
16-05-23 19:01	46
16-05-23 20:01	44
16-05-23 21:01	41
16-05-23 22:01	43
16-05-23 23:01	43
17-05-23 00:01	44
17-05-23 01:01	40
17-05-23 02:01	46
17-05-23 03:01	44
17-05-23 04:01	41
17-05-23 05:01	41
17-05-23 06:01	43
17-05-23 07:01	47
Average	46
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22-05-23 7:19	39
22-05-23 8:19	41
22-05-23 9:19	42
22-05-23 10:19	48
22-05-23 11:19	53
22-05-23 12:19	50
22-05-23 13:19	50
22-05-23 14:19	49
22-05-23 15:19	50
22-05-23 16:19	48
22-05-23 17:19	49
22-05-23 18:19	48
22-05-23 19:19	49
22-05-23 20:19	50
22-05-23 21:19	48
22-05-23 22:19	42
22-05-23 23:19	42
23-05-23 0:19	41
23-05-23 1:19	42
23-05-23 2:19	42
23-05-23 3:19	49
23-05-23 4:19	49
23-05-23 5:19	50
23-05-23 6:19	50
Average	47
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
27-05-23 07:30	66
27-05-23 08:30	72
27-05-23 09:30	70
27-05-23 10:30	65
27-05-23 11:30	68
27-05-23 12:30	69
27-05-23 13:30	60
27-05-23 14:30	62
27-05-23 15:30	60
27-05-23 16:30	56
27-05-23 17:30	50
27-05-23 18:30	60
27-05-23 19:30	62
27-05-23 20:30	64
27-05-23 21:30	65
27-05-23 22:30	60
27-05-23 23:30	55
28-05-23 00:30	54
28-05-23 01:30	58
28-05-23 02:30	63
28-05-23 03:30	60
28-05-23 04:30	65
28-05-23 05:30	61
28-05-23 06:30	63
Average	62
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS7A - Sheung Wo Che

Date and Time	TSP Concentration (µg/m³)
01-06-23 08:18	42
01-06-23 09:18	40
01-06-23 10:18	40
01-06-23 11:18	42
01-06-23 12:18	38
01-06-23 13:18	40
01-06-23 14:18	48
01-06-23 15:18	46
01-06-23 16:18	50
01-06-23 17:18	40
01-06-23 18:18	44
01-06-23 19:18	40
01-06-23 20:18	38
01-06-23 21:18	34
01-06-23 22:18	40
01-06-23 23:18	40
02-06-23 00:18	36
02-06-23 01:18	34
02-06-23 02:18	38
02-06-23 03:18	38
02-06-23 04:18	40
02-06-23 05:18	46
02-06-23 06:18	40
02-06-23 07:18	46
Average	41
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
07-06-23 07:44	50
07-06-23 08:44	54
07-06-23 09:44	64
07-06-23 10:44	68
07-06-23 11:44	74
07-06-23 12:44	58
07-06-23 13:44	60
07-06-23 14:44	70
07-06-23 15:44	76
07-06-23 16:44	66
07-06-23 17:44	64
07-06-23 18:44	60
07-06-23 19:44	62
07-06-23 20:44	68
07-06-23 21:44	78
07-06-23 22:44	64
07-06-23 23:44	54
08-06-23 00:44	52
08-06-23 01:44	58
08-06-23 02:44	56
08-06-23 03:44	60
08-06-23 04:44	48
08-06-23 05:44	52
08-06-23 06:44	62
Average	62
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
13-06-23 07:49	60
13-06-23 08:49	60
13-06-23 09:49	54
13-06-23 10:49	54
13-06-23 11:49	58
13-06-23 12:49	58
13-06-23 13:49	56
13-06-23 14:49	60
13-06-23 15:49	58
13-06-23 16:49	60
13-06-23 17:49	54
13-06-23 18:49	56
13-06-23 19:49	58
13-06-23 20:49	60
13-06-23 21:49	58
13-06-23 22:49	56
13-06-23 23:49	54
14-06-23 00:49	58
14-06-23 01:49	52
14-06-23 02:49	54
14-06-23 03:49	54
14-06-23 04:49	54
14-06-23 05:49	60
14-06-23 06:49	58
Average	57
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
19-06-23 8:05	44
19-06-23 9:05	48
19-06-23 10:05	46
19-06-23 11:05	48
19-06-23 12:05	42
19-06-23 13:05	40
19-06-23 14:05	40
19-06-23 15:05	50
19-06-23 16:05	48
19-06-23 17:05	44
19-06-23 18:05	40
19-06-23 19:05	40
19-06-23 20:05	36
19-06-23 21:05	40
19-06-23 22:05	36
19-06-23 23:05	36
20-06-23 0:05	44
20-06-23 1:05	38
20-06-23 2:05	34
20-06-23 3:05	36
20-06-23 4:05	42
20-06-23 5:05	46
20-06-23 6:05	44
20-06-23 7:05	50
Average	42
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
29-06-23 08:01	46
29-06-23 09:01	40
29-06-23 10:01	40
29-06-23 11:01	42
29-06-23 12:01	36
29-06-23 13:01	44
29-06-23 14:01	38
29-06-23 15:01	38
29-06-23 16:01	46
29-06-23 17:01	40
29-06-23 18:01	44
29-06-23 19:01	44
29-06-23 20:01	34
29-06-23 21:01	34
29-06-23 22:01	32
29-06-23 23:01	36
30-06-23 00:01	38
30-06-23 01:01	36
30-06-23 02:01	34
30-06-23 03:01	32
30-06-23 04:01	30
30-06-23 05:01	36
30-06-23 06:01	38
30-06-23 07:01	38
Average	38
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS7A - Sheung Wo Che

Date and Time	TSP Concentration (µg/m³)
05-07-23 08:05	46
05-07-23 09:05	50
05-07-23 10:05	48
05-07-23 11:05	48
05-07-23 12:05	50
05-07-23 13:05	42
05-07-23 14:05	44
05-07-23 15:05	44
05-07-23 16:05	50
05-07-23 17:05	42
05-07-23 18:05	44
05-07-23 19:05	48
05-07-23 20:05	42
05-07-23 21:05	40
05-07-23 22:05	38
05-07-23 23:05	44
06-07-23 00:05	44
06-07-23 01:05	36
06-07-23 02:05	38
06-07-23 03:05	38
06-07-23 04:05	40
06-07-23 05:05	44
06-07-23 06:05	42
06-07-23 07:05	46
Average	44
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
11-07-23 08:07	48
11-07-23 09:07	46
11-07-23 10:07	42
11-07-23 11:07	46
11-07-23 12:07	48
11-07-23 13:07	40
11-07-23 14:07	48
11-07-23 15:07	44
11-07-23 16:07	48
11-07-23 17:07	48
11-07-23 18:07	42
11-07-23 19:07	40
11-07-23 20:07	46
11-07-23 21:07	42
11-07-23 22:07	40
11-07-23 23:07	44
12-07-23 00:07	44
12-07-23 01:07	38
12-07-23 02:07	40
12-07-23 03:07	36
12-07-23 04:07	36
12-07-23 05:07	40
12-07-23 06:07	42
12-07-23 07:07	40
Average	43
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
18-07-23 07:56	28
18-07-23 08:56	30
18-07-23 09:56	28
18-07-23 10:56	30
18-07-23 11:56	30
18-07-23 12:56	32
18-07-23 13:56	28
18-07-23 14:56	32
18-07-23 15:56	30
18-07-23 16:56	30
18-07-23 17:56	32
18-07-23 18:56	28
18-07-23 19:56	24
18-07-23 20:56	24
18-07-23 21:56	22
18-07-23 22:56	26
18-07-23 23:56	24
19-07-23 00:56	24
19-07-23 01:56	22
19-07-23 02:56	26
19-07-23 03:56	28
19-07-23 04:56	28
19-07-23 05:56	26
19-07-23 06:56	28
Average	28
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
22-07-23 8:24	44
22-07-23 9:24	46
22-07-23 10:24	50
22-07-23 11:24	54
22-07-23 12:24	48
22-07-23 13:24	46
22-07-23 14:24	56
22-07-23 15:24	60
22-07-23 16:24	52
22-07-23 17:24	48
22-07-23 18:24	50
22-07-23 19:24	58
22-07-23 20:24	56
22-07-23 21:24	42
22-07-23 22:24	48
22-07-23 23:24	46
23-07-23 0:24	40
23-07-23 1:24	48
23-07-23 2:24	42
23-07-23 3:24	46
23-07-23 4:24	54
23-07-23 5:24	50
23-07-23 6:24	52
23-07-23 7:24	56
Average	50
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
29-07-23 08:08	42
29-07-23 09:08	40
29-07-23 10:08	40
29-07-23 11:08	44
29-07-23 12:08	38
29-07-23 13:08	42
29-07-23 14:08	42
29-07-23 15:08	44
29-07-23 16:08	46
29-07-23 17:08	40
29-07-23 18:08	36
29-07-23 19:08	38
29-07-23 20:08	38
29-07-23 21:08	42
29-07-23 22:08	40
29-07-23 23:08	36
30-07-23 00:08	36
30-07-23 01:08	38
30-07-23 02:08	34
30-07-23 03:08	36
30-07-23 04:08	38
30-07-23 05:08	40
30-07-23 06:08	42
30-07-23 07:08	44
Average	40
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS7A - Sheung Wo Che

Date and Time	TSP Concentration (µg/m³)
03-08-23 08:01	22
03-08-23 09:01	22
03-08-23 10:01	28
03-08-23 11:01	22
03-08-23 12:01	26
03-08-23 13:01	26
03-08-23 14:01	20
03-08-23 15:01	26
03-08-23 16:01	18
03-08-23 17:01	20
03-08-23 18:01	22
03-08-23 19:01	18
03-08-23 20:01	22
03-08-23 21:01	20
03-08-23 22:01	20
03-08-23 23:01	20
04-08-23 00:01	18
04-08-23 01:01	20
04-08-23 02:01	20
04-08-23 03:01	20
04-08-23 04:01	20
04-08-23 05:01	26
04-08-23 06:01	28
04-08-23 07:01	24
Average	22
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
09-08-23 07:31	32
09-08-23 08:31	30
09-08-23 09:31	30
09-08-23 10:31	30
09-08-23 11:31	28
09-08-23 12:31	30
09-08-23 13:31	32
09-08-23 14:31	28
09-08-23 15:31	28
09-08-23 16:31	30
09-08-23 17:31	32
09-08-23 18:31	32
09-08-23 19:31	26
09-08-23 20:31	24
09-08-23 21:31	26
09-08-23 22:31	24
09-08-23 23:31	24
10-08-23 00:31	28
10-08-23 01:31	26
10-08-23 02:31	24
10-08-23 03:31	22
10-08-23 04:31	22
10-08-23 05:31	26
10-08-23 06:31	28
Average	28
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
15-08-23 08:04	30
15-08-23 09:04	28
15-08-23 10:04	30
15-08-23 11:04	30
15-08-23 12:04	28
15-08-23 13:04	26
15-08-23 14:04	28
15-08-23 15:04	30
15-08-23 16:04	30
15-08-23 17:04	28
15-08-23 18:04	28
15-08-23 19:04	32
15-08-23 20:04	24
15-08-23 21:04	22
15-08-23 22:04	24
15-08-23 23:04	24
16-08-23 00:04	22
16-08-23 01:04	26
16-08-23 02:04	28
16-08-23 03:04	28
16-08-23 04:04	28
16-08-23 05:04	26
16-08-23 06:04	24
16-08-23 07:04	24
Average	27
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
21-08-23 7:58	32
21-08-23 8:58	30
21-08-23 9:58	32
21-08-23 10:58	32
21-08-23 11:58	28
21-08-23 12:58	28
21-08-23 13:58	26
21-08-23 14:58	30
21-08-23 15:58	30
21-08-23 16:58	28
21-08-23 17:58	30
21-08-23 18:58	28
21-08-23 19:58	26
21-08-23 20:58	24
21-08-23 21:58	24
21-08-23 22:58	24
21-08-23 23:58	26
22-08-23 0:58	24
22-08-23 1:58	22
22-08-23 2:58	24
22-08-23 3:58	26
22-08-23 4:58	28
22-08-23 5:58	28
22-08-23 6:58	24
Average	27
Action Level	171
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
26-08-23 09:11	44
26-08-23 10:11	41
26-08-23 11:11	37
26-08-23 12:11	39
26-08-23 13:11	50
26-08-23 14:11	59
26-08-23 15:11	50
26-08-23 16:11	46
26-08-23 17:11	44
26-08-23 18:11	41
26-08-23 19:11	37
26-08-23 20:11	37
26-08-23 21:11	48
26-08-23 22:11	50
26-08-23 23:11	48
27-08-23 00:11	46
27-08-23 01:11	44
27-08-23 02:11	39
27-08-23 03:11	37
27-08-23 04:11	37
27-08-23 05:11	37
27-08-23 06:11	46
27-08-23 07:11	47
27-08-23 08:11	50
Average	44
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 12 - Fung Wo Estate

Date and Time	TSP Concentration (µg/m³)
04-05-23 08:05	41
04-05-23 09:05	44
04-05-23 10:05	41
04-05-23 11:05	47
04-05-23 12:05	48
04-05-23 13:05	43
04-05-23 14:05	44
04-05-23 15:05	39
04-05-23 16:05	40
04-05-23 17:05	34
04-05-23 18:05	36
04-05-23 19:05	39
04-05-23 20:05	37
04-05-23 21:05	34
04-05-23 22:05	34
04-05-23 23:05	36
05-05-23 00:05	39
05-05-23 01:05	34
05-05-23 02:05	36
05-05-23 03:05	37
05-05-23 04:05	34
05-05-23 05:05	33
05-05-23 06:05	39
05-05-23 07:05	40
Average	39
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
10-05-23 07:30	35
10-05-23 08:30	34
10-05-23 09:30	36
10-05-23 10:30	34
10-05-23 11:30	32
10-05-23 12:30	32
10-05-23 13:30	34
10-05-23 14:30	35
10-05-23 15:30	36
10-05-23 16:30	36
10-05-23 17:30	38
10-05-23 18:30	39
10-05-23 19:30	35
10-05-23 20:30	34
10-05-23 21:30	32
10-05-23 22:30	32
10-05-23 23:30	31
11-05-23 00:30	32
11-05-23 01:30	31
11-05-23 02:30	31
11-05-23 03:30	31
11-05-23 04:30	32
11-05-23 05:30	32
11-05-23 06:30	34
Average	34
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
16-05-23 08:11	39
16-05-23 09:11	39
16-05-23 10:11	41
16-05-23 11:11	40
16-05-23 12:11	37
16-05-23 13:11	39
16-05-23 14:11	40
16-05-23 15:11	44
16-05-23 16:11	40
16-05-23 17:11	47
16-05-23 18:11	34
16-05-23 19:11	39
16-05-23 20:11	37
16-05-23 21:11	34
16-05-23 22:11	36
16-05-23 23:11	36
17-05-23 00:11	40
17-05-23 01:11	41
17-05-23 02:11	39
17-05-23 03:11	39
17-05-23 04:11	37
17-05-23 05:11	34
17-05-23 06:11	40
17-05-23 07:11	44
Average	39
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
22-05-23 07:32	34
22-05-23 08:32	32
22-05-23 09:32	32
22-05-23 10:32	34
22-05-23 11:32	35
22-05-23 12:32	34
22-05-23 13:32	34
22-05-23 14:32	35
22-05-23 15:32	35
22-05-23 16:32	34
22-05-23 17:32	27
22-05-23 18:32	36
22-05-23 19:32	35
22-05-23 20:32	34
22-05-23 21:32	34
22-05-23 22:32	32
22-05-23 23:32	32
23-05-23 00:32	28
23-05-23 01:32	41
23-05-23 02:32	35
23-05-23 03:32	38
23-05-23 04:32	39
23-05-23 05:32	39
23-05-23 6:32	36
Average	34
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
27-05-23 07:48	44
27-05-23 08:48	57
27-05-23 09:48	63
27-05-23 10:48	59
27-05-23 11:48	76
27-05-23 12:48	72
27-05-23 13:48	72
27-05-23 14:48	80
27-05-23 15:48	72
27-05-23 16:48	65
27-05-23 17:48	74
27-05-23 18:48	72
27-05-23 19:48	46
27-05-23 20:48	84
27-05-23 21:48	61
27-05-23 22:48	74
27-05-23 23:48	76
28-05-23 00:48	69
28-05-23 01:48	67
28-05-23 02:48	59
28-05-23 03:48	46
28-05-23 04:48	44
28-05-23 05:48	69
28-05-23 06:48	65
Average	65
Action Level	168
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 12 - Fung Wo Estate

Date and Time	TSP Concentration (µg/m³)
01-06-23 08:04	43
01-06-23 09:04	45
01-06-23 10:04	41
01-06-23 11:04	49
01-06-23 12:04	41
01-06-23 13:04	37
01-06-23 14:04	39
01-06-23 15:04	41
01-06-23 16:04	43
01-06-23 17:04	39
01-06-23 18:04	37
01-06-23 19:04	39
01-06-23 20:04	39
01-06-23 21:04	41
01-06-23 22:04	41
01-06-23 23:04	43
02-06-23 00:04	41
02-06-23 01:04	43
02-06-23 02:04	45
02-06-23 03:04	41
02-06-23 04:04	45
02-06-23 05:04	41
02-06-23 06:04	45
02-06-23 07:04	45
Average	42
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
07-06-23 08:12	59
07-06-23 09:12	76
07-06-23 10:12	69
07-06-23 11:12	74
07-06-23 12:12	69
07-06-23 13:12	61
07-06-23 14:12	78
07-06-23 15:12	69
07-06-23 16:12	63
07-06-23 17:12	67
07-06-23 18:12	65
07-06-23 19:12	61
07-06-23 20:12	57
07-06-23 21:12	84
07-06-23 22:12	59
07-06-23 23:12	67
08-06-23 00:12	65
08-06-23 01:12	69
08-06-23 02:12	71
08-06-23 03:12	63
08-06-23 04:12	67
08-06-23 05:12	51
08-06-23 06:12	55
08-06-23 07:12	65
Average	66
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
13-06-23 07:40	55
13-06-23 08:40	53
13-06-23 09:40	57
13-06-23 10:40	59
13-06-23 11:40	61
13-06-23 12:40	59
13-06-23 13:40	63
13-06-23 14:40	63
13-06-23 15:40	59
13-06-23 16:40	61
13-06-23 17:40	63
13-06-23 18:40	57
13-06-23 19:40	59
13-06-23 20:40	59
13-06-23 21:40	61
13-06-23 22:40	63
13-06-23 23:40	63
14-06-23 00:40	57
14-06-23 01:40	59
14-06-23 02:40	55
14-06-23 03:40	59
14-06-23 04:40	59
14-06-23 05:40	63
14-06-23 06:40	61
Average	60
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
19-06-23 08:14	47
19-06-23 09:14	45
19-06-23 10:14	45
19-06-23 11:14	49
19-06-23 12:14	51
19-06-23 13:14	43
19-06-23 14:14	41
19-06-23 15:14	47
19-06-23 16:14	43
19-06-23 17:14	45
19-06-23 18:14	45
19-06-23 19:14	47
19-06-23 20:14	41
19-06-23 21:14	43
19-06-23 22:14	37
19-06-23 23:14	39
20-06-23 00:14	39
20-06-23 01:14	43
20-06-23 02:14	41
20-06-23 03:14	37
20-06-23 04:14	37
20-06-23 05:14	43
20-06-23 06:14	41
20-06-23 7:14	39
Average	43
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
29-06-23 08:10	59
29-06-23 09:10	49
29-06-23 10:10	47
29-06-23 11:10	43
29-06-23 12:10	43
29-06-23 13:10	47
29-06-23 14:10	41
29-06-23 15:10	43
29-06-23 16:10	49
29-06-23 17:10	41
29-06-23 18:10	41
29-06-23 19:10	43
29-06-23 20:10	43
29-06-23 21:10	37
29-06-23 22:10	39
29-06-23 23:10	45
30-06-23 00:10	37
30-06-23 01:10	32
30-06-23 02:10	32
30-06-23 03:10	41
30-06-23 04:10	43
30-06-23 05:10	39
30-06-23 06:10	34
30-06-23 07:10	45
Average	42
Action Level	168
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 12 - Fung Wo Estate

Date and Time	TSP Concentration (µg/m³)
05-07-23 08:15	45
05-07-23 09:15	49
05-07-23 10:15	51
05-07-23 11:15	57
05-07-23 12:15	49
05-07-23 13:15	47
05-07-23 14:15	47
05-07-23 15:15	45
05-07-23 16:15	53
05-07-23 17:15	49
05-07-23 18:15	43
05-07-23 19:15	47
05-07-23 20:15	45
05-07-23 21:15	41
05-07-23 22:15	49
05-07-23 23:15	41
06-07-23 00:15	41
06-07-23 01:15	43
06-07-23 02:15	37
06-07-23 03:15	37
06-07-23 04:15	39
06-07-23 05:15	43
06-07-23 06:15	45
06-07-23 07:15	41
Average	45
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
11-07-23 08:16	51
11-07-23 09:16	55
11-07-23 10:16	43
11-07-23 11:16	45
11-07-23 12:16	53
11-07-23 13:16	47
11-07-23 14:16	43
11-07-23 15:16	45
11-07-23 16:16	57
11-07-23 17:16	43
11-07-23 18:16	49
11-07-23 19:16	41
11-07-23 20:16	47
11-07-23 21:16	43
11-07-23 22:16	45
11-07-23 23:16	45
12-07-23 00:16	49
12-07-23 01:16	41
12-07-23 02:16	41
12-07-23 03:16	45
12-07-23 04:16	41
12-07-23 05:16	37
12-07-23 06:16	43
12-07-23 07:16	45
Average	46
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
18-07-23 07:44	30
18-07-23 08:44	30
18-07-23 09:44	28
18-07-23 10:44	32
18-07-23 11:44	32
18-07-23 12:44	28
18-07-23 13:44	30
18-07-23 14:44	34
18-07-23 15:44	34
18-07-23 16:44	34
18-07-23 17:44	30
18-07-23 18:44	32
18-07-23 19:44	32
18-07-23 20:44	32
18-07-23 21:44	28
18-07-23 22:44	22
18-07-23 23:44	26
19-07-23 00:44	20
19-07-23 01:44	20
19-07-23 02:44	24
19-07-23 03:44	27
19-07-23 04:44	20
19-07-23 05:44	26
19-07-23 06:44	22
Average	28
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
22-07-23 08:31	47
22-07-23 09:31	53
22-07-23 10:31	45
22-07-23 11:31	43
22-07-23 12:31	39
22-07-23 13:31	47
22-07-23 14:31	55
22-07-23 15:31	58
22-07-23 16:31	61
22-07-23 17:31	65
22-07-23 18:31	63
22-07-23 19:31	55
22-07-23 20:31	57
22-07-23 21:31	59
22-07-23 22:31	51
22-07-23 23:31	53
23-07-23 00:31	45
23-07-23 01:31	41
23-07-23 02:31	39
23-07-23 03:31	43
23-07-23 04:31	49
23-07-23 05:31	51
23-07-23 06:31	55
23-07-23 7:31	47
Average	51
Action Level	168
Limit Level	260

Date and Time	TSP Concentration (µg/m³)
29-07-23 08:17	47
29-07-23 09:17	49
29-07-23 10:17	45
29-07-23 11:17	41
29-07-23 12:17	49
29-07-23 13:17	47
29-07-23 14:17	47
29-07-23 15:17	43
29-07-23 16:17	45
29-07-23 17:17	41
29-07-23 18:17	47
29-07-23 19:17	49
29-07-23 20:17	43
29-07-23 21:17	41
29-07-23 22:17	41
29-07-23 23:17	45
30-07-23 00:17	45
30-07-23 01:17	45
30-07-23 02:17	37
30-07-23 03:17	39
30-07-23 04:17	39
30-07-23 05:17	443
30-07-23 06:17	45
30-07-23 07:17	41
Average	61
Action Level	168
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 12 - Fung Wo Estate

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
03-08-23 07:46	24
03-08-23 08:46	20
03-08-23 09:46	20
03-08-23 10:46	20
03-08-23 11:46	26
03-08-23 12:46	30
03-08-23 13:46	30
03-08-23 14:46	28
03-08-23 15:46	18
03-08-23 16:46	20
03-08-23 17:46	24
03-08-23 18:46	18
03-08-23 19:46	18
03-08-23 20:46	22
03-08-23 21:46	20
03-08-23 22:46	18
03-08-23 23:46	22
04-08-23 00:46	20
04-08-23 01:46	18
04-08-23 02:46	20
04-08-23 03:46	26
04-08-23 04:46	22
04-08-23 05:46	18
04-08-23 06:46	22
Average	22
Action Level	168
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
09-08-23 08:14	34
09-08-23 09:14	34
09-08-23 10:14	30
09-08-23 11:14	28
09-08-23 12:14	28
09-08-23 13:14	28
09-08-23 14:14	30
09-08-23 15:14	32
09-08-23 16:14	30
09-08-23 17:14	30
09-08-23 18:14	32
09-08-23 19:14	32
09-08-23 20:14	34
09-08-23 21:14	32
09-08-23 22:14	30
09-08-23 23:14	34
10-08-23 00:14	32
10-08-23 01:14	30
10-08-23 02:14	22
10-08-23 03:14	22
10-08-23 04:14	24
10-08-23 05:14	26
10-08-23 06:14	22
10-08-23 07:14	28
Average	29
Action Level	168
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
15-08-23 07:40	32
15-08-23 08:40	28
15-08-23 09:40	30
15-08-23 10:40	24
15-08-23 11:40	28
15-08-23 12:40	26
15-08-23 13:40	32
15-08-23 14:40	30
15-08-23 15:40	28
15-08-23 16:40	26
15-08-23 17:40	28
15-08-23 18:40	24
15-08-23 19:40	24
15-08-23 20:40	26
15-08-23 21:40	32
15-08-23 22:40	32
15-08-23 23:40	28
16-08-23 00:40	24
16-08-23 01:40	26
16-08-23 02:40	32
16-08-23 03:40	30
16-08-23 04:40	26
16-08-23 05:40	30
16-08-23 06:40	28
Average	28
Action Level	168
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
21-08-23 07:46	32
21-08-23 08:46	32
21-08-23 09:46	34
21-08-23 10:46	34
21-08-23 11:46	30
21-08-23 12:46	30
21-08-23 13:46	28
21-08-23 14:46	32
21-08-23 15:46	34
21-08-23 16:46	34
21-08-23 17:46	30
21-08-23 18:46	32
21-08-23 19:46	32
21-08-23 20:46	32
21-08-23 21:46	28
21-08-23 22:46	24
21-08-23 23:46	26
22-08-23 00:46	24
22-08-23 01:46	24
22-08-23 02:46	26
22-08-23 03:46	26
22-08-23 04:46	22
22-08-23 05:46	20
22-08-23 06:46	24
Average	29
Action Level	168
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
26-08-23 09:34	45
26-08-23 10:34	34
26-08-23 11:34	27
26-08-23 12:34	36
26-08-23 13:34	25
26-08-23 14:34	36
26-08-23 15:34	30
26-08-23 16:34	27
26-08-23 17:34	28
26-08-23 18:34	23
26-08-23 19:34	23
26-08-23 20:34	23
26-08-23 21:34	27
26-08-23 22:34	21
26-08-23 23:34	27
27-08-23 00:34	28
27-08-23 01:34	30
27-08-23 02:34	30
27-08-23 03:34	32
27-08-23 04:34	23
27-08-23 05:34	25
27-08-23 06:34	27
27-08-23 07:34	28
27-08-23 08:34	30
Average	29
Action Level	168
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 17 - Wo Che Estate

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
04-05-23 08:14	39
04-05-23 09:14	40
04-05-23 10:14	44
04-05-23 11:14	46
04-05-23 12:14	41
04-05-23 13:14	47
04-05-23 14:14	46
04-05-23 15:14	41
04-05-23 16:14	39
04-05-23 17:14	34
04-05-23 18:14	37
04-05-23 19:14	36
04-05-23 20:14	36
04-05-23 21:14	34
04-05-23 22:14	39
04-05-23 23:14	39
05-05-23 00:14	34
05-05-23 01:14	37
05-05-23 02:14	40
05-05-23 03:14	41
05-05-23 04:14	39
05-05-23 05:14	41
05-05-23 06:14	41
05-05-23 07:14	43
Average	40
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
10-05-23 07:49	39
10-05-23 08:49	41
10-05-23 09:49	41
10-05-23 10:49	42
10-05-23 11:49	48
10-05-23 12:49	48
10-05-23 13:49	49
10-05-23 14:49	48
10-05-23 15:49	45
10-05-23 16:49	46
10-05-23 17:49	46
10-05-23 18:49	48
10-05-23 19:49	49
10-05-23 20:49	42
10-05-23 21:49	41
10-05-23 22:49	42
10-05-23 23:49	41
11-05-23 00:49	42
11-05-23 01:49	42
11-05-23 02:49	39
11-05-23 03:49	41
11-05-23 04:49	41
11-05-23 05:49	42
11-05-23 06:49	39
Average	43
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
16-05-23 08:19	41
16-05-23 09:19	44
16-05-23 10:19	43
16-05-23 11:19	39
16-05-23 12:19	40
16-05-23 13:19	46
16-05-23 14:19	50
16-05-23 15:19	44
16-05-23 16:19	43
16-05-23 17:19	47
16-05-23 18:19	41
16-05-23 19:19	41
16-05-23 20:19	37
16-05-23 21:19	40
16-05-23 22:19	43
16-05-23 23:19	39
17-05-23 00:19	39
17-05-23 01:19	34
17-05-23 02:19	39
17-05-23 03:19	37
17-05-23 04:19	36
17-05-23 05:19	40
17-05-23 06:19	43
17-05-23 07:19	41
Average	41
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22-05-23 07:50	42
22-05-23 08:50	45
22-05-23 09:50	48
22-05-23 10:50	49
22-05-23 11:50	49
22-05-23 12:50	48
22-05-23 13:50	50
22-05-23 14:50	48
22-05-23 15:50	49
22-05-23 16:50	49
22-05-23 17:50	48
22-05-23 18:50	43
22-05-23 19:50	42
22-05-23 20:50	45
22-05-23 21:50	42
22-05-23 22:50	41
22-05-23 23:50	42
23-05-23 00:50	41
23-05-23 01:50	42
23-05-23 02:50	52
23-05-23 03:50	50
23-05-23 04:50	50
23-05-23 05:50	48
23-05-23 06:50	49
Average	46
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
27-05-23 08:22	34
27-05-23 09:22	37
27-05-23 10:22	45
27-05-23 11:22	53
27-05-23 12:22	50
27-05-23 13:22	63
27-05-23 14:22	50
27-05-23 15:22	68
27-05-23 16:22	76
27-05-23 17:22	79
27-05-23 18:22	90
27-05-23 19:22	98
27-05-23 20:22	76
27-05-23 21:22	79
27-05-23 22:22	63
27-05-23 23:22	55
28-05-23 00:22	45
28-05-23 01:22	42
28-05-23 02:22	55
28-05-23 03:22	63
28-05-23 04:22	60
28-05-23 05:22	53
28-05-23 06:22	50
28-05-23 07:22	63
Average	60
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 17 - Wo Che Estate

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
01-06-23 07:52	45
01-06-23 08:52	47
01-06-23 09:52	47
01-06-23 10:52	43
01-06-23 11:52	49
01-06-23 12:52	49
01-06-23 13:52	47
01-06-23 14:52	43
01-06-23 15:52	47
01-06-23 16:52	47
01-06-23 17:52	45
01-06-23 18:52	41
01-06-23 19:52	41
01-06-23 20:52	41
01-06-23 21:52	39
01-06-23 22:52	43
01-06-23 23:52	41
02-06-23 00:52	43
02-06-23 01:52	49
02-06-23 02:52	47
02-06-23 03:52	47
02-06-23 04:52	45
02-06-23 05:52	49
02-06-23 06:52	47
Average	45
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
07-06-23 08:23	65
07-06-23 09:23	57
07-06-23 10:23	61
07-06-23 11:23	63
07-06-23 12:23	55
07-06-23 13:23	47
07-06-23 14:23	59
07-06-23 15:23	63
07-06-23 16:23	55
07-06-23 17:23	57
07-06-23 18:23	67
07-06-23 19:23	51
07-06-23 20:23	57
07-06-23 21:23	47
07-06-23 22:23	55
07-06-23 23:23	41
08-06-23 00:23	59
08-06-23 01:23	61
08-06-23 02:23	69
08-06-23 03:23	63
08-06-23 04:23	71
08-06-23 05:23	61
08-06-23 06:23	59
08-06-23 07:23	53
Average	58
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
13-06-23 07:30	59
13-06-23 08:30	59
13-06-23 09:30	63
13-06-23 10:30	61
13-06-23 11:30	59
13-06-23 12:30	57
13-06-23 13:30	61
13-06-23 14:30	63
13-06-23 15:30	59
13-06-23 16:30	61
13-06-23 17:30	61
13-06-23 18:30	57
13-06-23 19:30	57
13-06-23 20:30	59
13-06-23 21:30	61
13-06-23 22:30	53
13-06-23 23:30	59
14-06-23 00:30	59
14-06-23 01:30	55
14-06-23 02:30	57
14-06-23 03:30	59
14-06-23 04:30	61
14-06-23 05:30	61
14-06-23 06:30	59
Average	59
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
19-06-23 08:22	49
19-06-23 09:22	43
19-06-23 10:22	39
19-06-23 11:22	51
19-06-23 12:22	49
19-06-23 13:22	47
19-06-23 14:22	39
19-06-23 15:22	41
19-06-23 16:22	41
19-06-23 17:22	49
19-06-23 18:22	43
19-06-23 19:22	39
19-06-23 20:22	43
19-06-23 21:22	45
19-06-23 22:22	45
19-06-23 23:22	39
20-06-23 00:22	35
20-06-23 01:22	45
20-06-23 02:22	43
20-06-23 03:22	43
20-06-23 04:22	41
20-06-23 05:22	39
20-06-23 06:22	39
20-06-23 07:22	45
Average	43
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
29-06-23 08:18	43
29-06-23 09:18	43
29-06-23 10:18	39
29-06-23 11:18	45
29-06-23 12:18	39
29-06-23 13:18	51
29-06-23 14:18	43
29-06-23 15:18	47
29-06-23 16:18	45
29-06-23 17:18	39
29-06-23 18:18	39
29-06-23 19:18	41
29-06-23 20:18	41
29-06-23 21:18	43
29-06-23 22:18	37
29-06-23 23:18	37
30-06-23 00:18	39
30-06-23 01:18	35
30-06-23 02:18	37
30-06-23 03:18	45
30-06-23 04:18	41
30-06-23 05:18	39
30-06-23 06:18	39
30-06-23 07:18	35
Average	41
Action Level	171
Limit Level	260

Remark

1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 17 - Wo Che Estate

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
05-07-23 08:23	47
05-07-23 09:23	49
05-07-23 10:23	53
05-07-23 11:23	43
05-07-23 12:23	49
05-07-23 13:23	47
05-07-23 14:23	45
05-07-23 15:23	41
05-07-23 16:23	39
05-07-23 17:23	45
05-07-23 18:23	47
05-07-23 19:23	43
05-07-23 20:23	41
05-07-23 21:23	43
05-07-23 22:23	45
05-07-23 23:23	45
06-07-23 00:23	39
06-07-23 01:23	35
06-07-23 02:23	39
06-07-23 03:23	43
06-07-23 04:23	37
06-07-23 05:23	41
06-07-23 06:23	39
06-07-23 07:23	41
Average	43
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
11-07-23 08:24	43
11-07-23 09:24	39
11-07-23 10:24	47
11-07-23 11:24	43
11-07-23 12:24	41
11-07-23 13:24	47
11-07-23 14:24	49
11-07-23 15:24	45
11-07-23 16:24	45
11-07-23 17:24	41
11-07-23 18:24	39
11-07-23 19:24	39
11-07-23 20:24	35
11-07-23 21:24	37
11-07-23 22:24	41
11-07-23 23:24	39
12-07-23 00:24	43
12-07-23 01:24	39
12-07-23 02:24	39
12-07-23 03:24	41
12-07-23 04:24	41
12-07-23 05:24	41
12-07-23 06:24	45
12-07-23 07:24	39
Average	42
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
18-07-23 07:31	27
18-07-23 08:31	27
18-07-23 09:31	33
18-07-23 10:31	29
18-07-23 11:31	33
18-07-23 12:31	31
18-07-23 13:31	33
18-07-23 14:31	33
18-07-23 15:31	29
18-07-23 16:31	29
18-07-23 17:31	27
18-07-23 18:31	31
18-07-23 19:31	29
18-07-23 20:31	29
18-07-23 21:31	27
18-07-23 22:31	25
18-07-23 23:31	23
19-07-23 00:31	23
19-07-23 01:31	19
19-07-23 02:31	19
19-07-23 03:31	23
19-07-23 04:31	21
19-07-23 05:31	19
19-07-23 06:31	25
Average	27
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
22-07-23 08:43	51
22-07-23 09:43	53
22-07-23 10:43	45
22-07-23 11:43	43
22-07-23 12:43	49
22-07-23 13:43	55
22-07-23 14:43	47
22-07-23 15:43	57
22-07-23 16:43	53
22-07-23 17:43	61
22-07-23 18:43	63
22-07-23 19:43	69
22-07-23 20:43	55
22-07-23 21:43	59
22-07-23 22:43	61
22-07-23 23:43	67
23-07-23 00:43	57
23-07-23 01:43	59
23-07-23 02:43	53
23-07-23 03:43	49
23-07-23 04:43	57
23-07-23 05:43	55
23-07-23 06:43	51
23-07-23 07:43	53
Average	55
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
29-07-23 08:25	39
29-07-23 09:25	39
29-07-23 10:25	43
29-07-23 11:25	41
29-07-23 12:25	47
29-07-23 13:25	49
29-07-23 14:25	39
29-07-23 15:25	41
29-07-23 16:25	45
29-07-23 17:25	41
29-07-23 18:25	41
29-07-23 19:25	39
29-07-23 20:25	43
29-07-23 21:25	37
29-07-23 22:25	35
29-07-23 23:25	33
30-07-23 00:25	35
30-07-23 01:25	35
30-07-23 02:25	39
30-07-23 03:25	39
30-07-23 04:25	35
30-07-23 05:25	37
30-07-23 06:25	41
30-07-23 07:25	39
Average	40
Action Level	171
Limit Level	260

Remark

1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

**24-hour TSP Impact Monitoring Result for
NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)**

AMS 17 - Wo Che Estate

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
03-08-23 07:32	25
03-08-23 08:32	29
03-08-23 09:32	23
03-08-23 10:32	23
03-08-23 11:32	25
03-08-23 12:32	23
03-08-23 13:32	19
03-08-23 14:32	25
03-08-23 15:32	19
03-08-23 16:32	19
03-08-23 17:32	27
03-08-23 18:32	19
03-08-23 19:32	21
03-08-23 20:32	25
03-08-23 21:32	19
03-08-23 22:32	25
03-08-23 23:32	27
04-08-23 00:32	23
04-08-23 01:32	23
04-08-23 02:32	27
04-08-23 03:32	29
04-08-23 04:32	27
04-08-23 05:32	25
04-08-23 06:32	25
Average	24
Action Level	171
Limit Level	260



Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
09-08-23 08:02	32
09-08-23 09:02	34
09-08-23 10:02	32
09-08-23 11:02	32
09-08-23 12:02	30
09-08-23 13:02	28
09-08-23 14:02	30
09-08-23 15:02	34
09-08-23 16:02	34
09-08-23 17:02	32
09-08-23 18:02	28
09-08-23 19:02	30
09-08-23 20:02	30
09-08-23 21:02	30
09-08-23 22:02	28
09-08-23 23:02	26
10-08-23 00:02	24
10-08-23 01:02	28
10-08-23 02:02	22
10-08-23 03:02	22
10-08-23 04:02	20
10-08-23 05:02	20
10-08-23 06:02	22
10-08-23 07:02	30
Average	28
Action Level	171
Limit Level	260



Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
15-08-23 07:52	33
15-08-23 08:52	29
15-08-23 09:52	33
15-08-23 10:52	25
15-08-23 11:52	31
15-08-23 12:52	29
15-08-23 13:52	33
15-08-23 14:52	25
15-08-23 15:52	29
15-08-23 16:52	29
15-08-23 17:52	31
15-08-23 18:52	27
15-08-23 19:52	25
15-08-23 20:52	25
15-08-23 21:52	31
15-08-23 22:52	29
15-08-23 23:52	25
16-08-23 00:52	29
16-08-23 01:52	31
16-08-23 02:52	27
16-08-23 03:52	25
16-08-23 04:52	29
16-08-23 05:52	29
16-08-23 06:52	25
Average	29
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
21-08-23 07:32	32
21-08-23 08:32	32
21-08-23 09:32	30
21-08-23 10:32	30
21-08-23 11:32	30
21-08-23 12:32	30
21-08-23 13:32	34
21-08-23 14:32	32
21-08-23 15:32	30
21-08-23 16:32	30
21-08-23 17:32	28
21-08-23 18:32	28
21-08-23 19:32	30
21-08-23 20:32	32
21-08-23 21:32	28
21-08-23 22:32	26
21-08-23 23:32	26
22-08-23 00:32	24
22-08-23 01:32	20
22-08-23 02:32	20
22-08-23 03:32	22
22-08-23 04:32	22
22-08-23 05:32	22
22-08-23 06:32	26
Average	28
Action Level	171
Limit Level	260

Date and Time	TSP Concentration ($\mu\text{g}/\text{m}^3$)
26-08-23 09:58	32
26-08-23 10:58	22
26-08-23 11:58	18
26-08-23 12:58	22
26-08-23 13:58	24
26-08-23 14:58	22
26-08-23 15:58	20
26-08-23 16:58	36
26-08-23 17:58	24
26-08-23 18:58	28
26-08-23 19:58	28
26-08-23 20:58	22
26-08-23 21:58	24
26-08-23 22:58	26
26-08-23 23:58	28
27-08-23 00:58	22
27-08-23 01:58	20
27-08-23 02:58	20
27-08-23 03:58	18
27-08-23 04:58	18
27-08-23 05:58	14
27-08-23 06:58	22
27-08-23 07:58	24
27-08-23 08:58	24
Average	23
Action Level	171
Limit Level	260

- Remark
1. Actual monitoring may be subjected to change due to any safety concern or adverse weather condition.
 2. The Impact Air Monitoring Stations to be monitored should be selected based on the prevailing wind direction and their proximity to the active construction works.

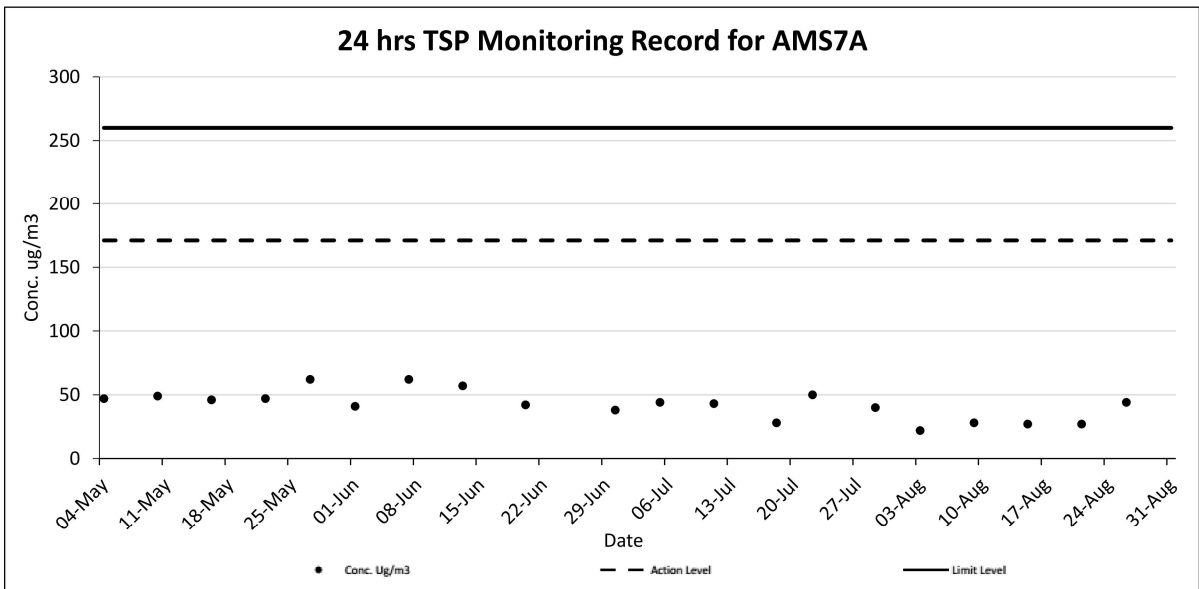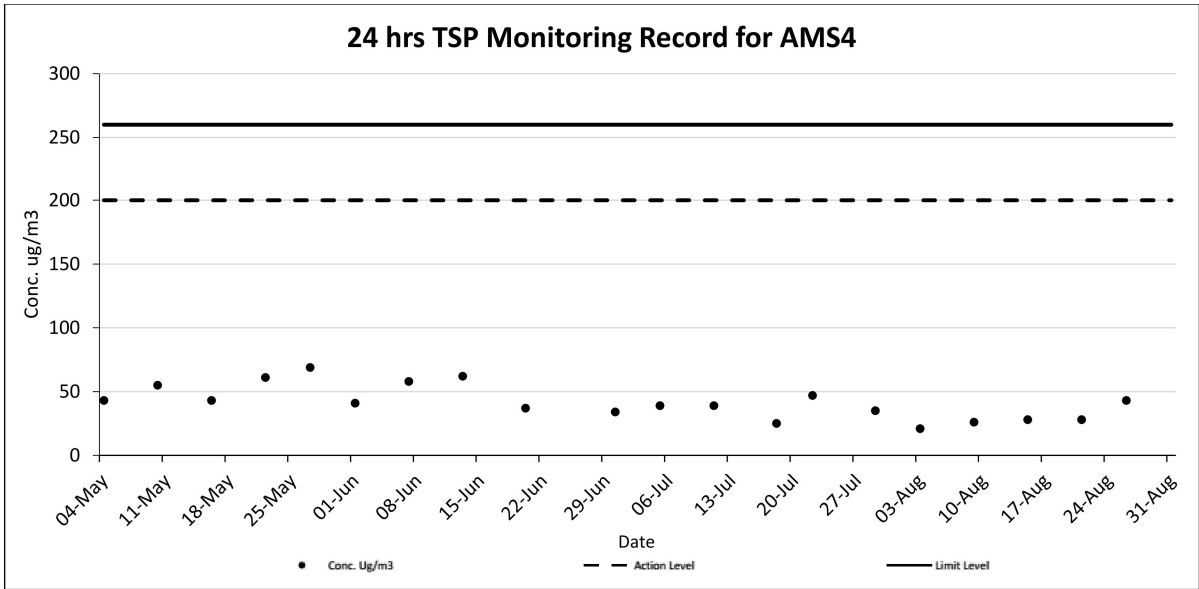

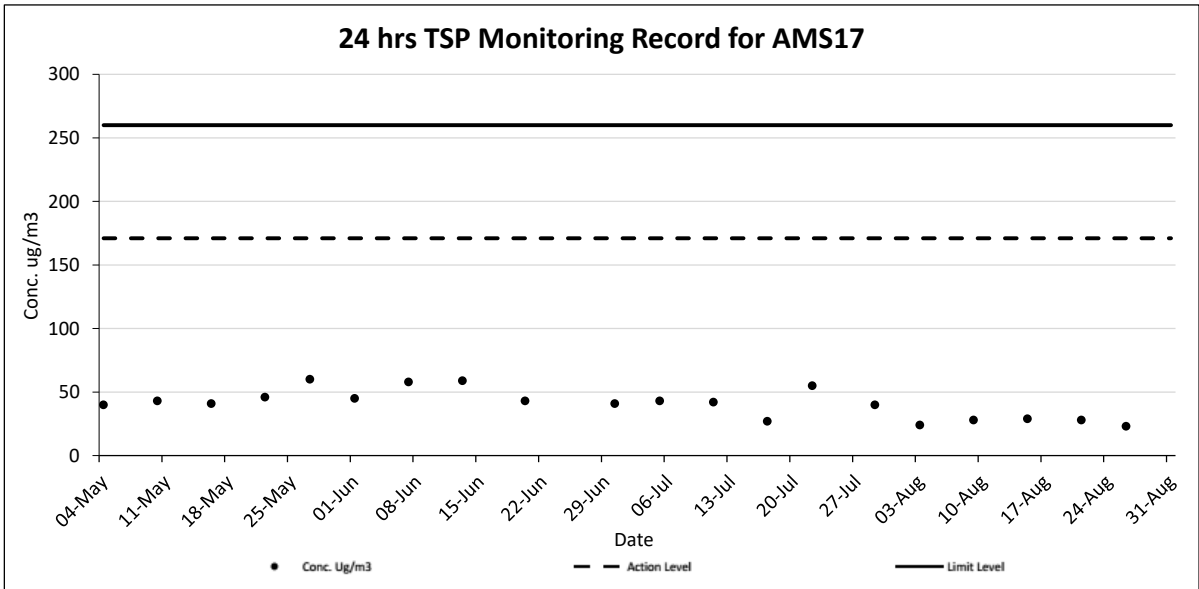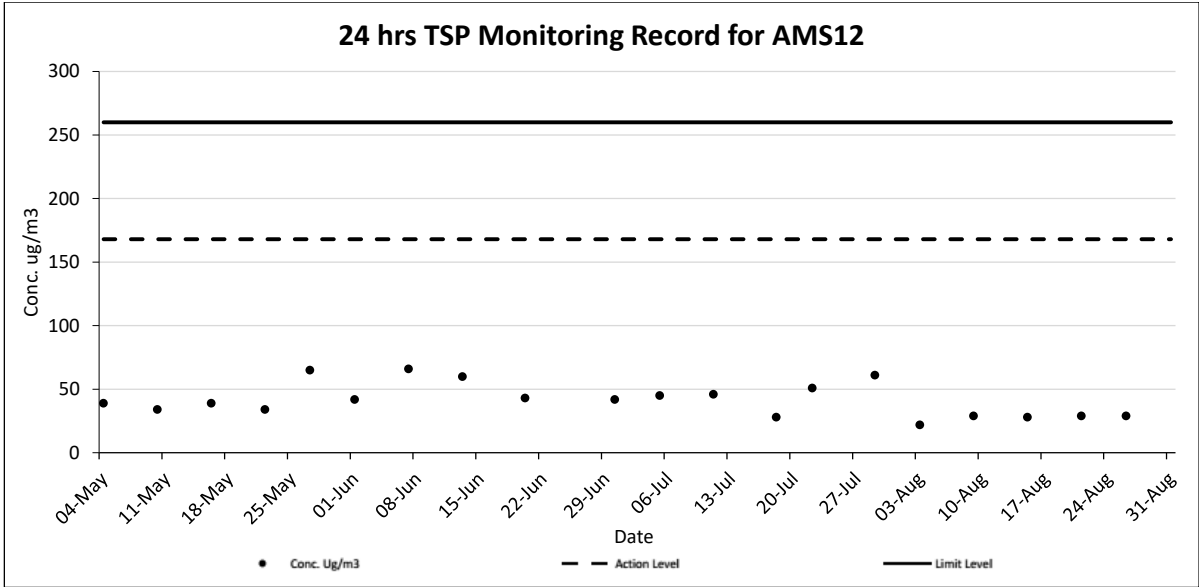

Impact Noise Monitoring Result for NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

NMS 1 Scenery Court

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	17:16	61.2	59.5	62.5	75	61.2	Fine	0.3
10-May-23	9:34	61.3	59.5	64.5	75	61.3	Overcast	0.6
16-May-23	8:30	66.0	64.0	68.0	75	66.0	Fine	0.4
22-May-23	9:39	60.3	58.5	63.5	75	60.3	Fine	0.2
01-Jun-23	9:44	61.4	58.0	64.5	75	61.4	Fine	0.7
07-Jun-23	8:20	63.7	60.5	65.5	75	63.7	Overcast	0.3
13-Jun-23	8:26	66.4	62.5	69.0	75	66.4	Fine	0.7
19-Jun-23	8:00	67.0	65.0	69.0	75	67.0	Fine	0.6
29-Jun-23	17:55	62.4	60.0	64.5	75	62.4	Fine	0.3
05-Jul-23	13:00	61.1	59.0	64.0	75	61.1	Fine	0.4
11-Jul-23	8:00	63.5	61.0	66.0	75	63.5	Sunny	0.4
18-Jul-23	17:38	63.8	60.5	65.0	75	63.8	Overcast	0.2
28-Jul-23	10:34	61.5	60.0	63.5	75	61.5	Fine	0.3
03-Aug-23	13:49	62.4	59.5	64.0	75	62.4	Fine	0.2
09-Aug-23	16:57	66.4	63.0	67.5	75	66.4	Sunny	0.3
15-Aug-23	13:49	61.6	58.5	63.0	75	61.6	Overcast	0.2
21-Aug-23	16:58	65.7	62.5	66.0	75	65.7	Fine	0.3

NMS 2 Villa Le Parc

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	16:35	52.1	50.0	54.0	75	52.1	Fine	0.2
10-May-23	10:54	59.6	54.5	63.0	75	59.6	Overcast	0.7
16-May-23	11:09	59.0	58.0	61.0	75	59.0	Fine	0.0
22-May-23	10:59	58.4	55.0	62.5	75	58.4	Fine	0.2
01-Jun-23	11:04	57.9	54.0	59.5	75	57.9	Fine	0.6
07-Jun-23	09:54	51.2	49.5	52.3	75	51.2	Overcast	0.5
13-Jun-23	08:54	61.4	58.0	64.0	75	61.4	Fine	0.3
19-Jun-23	11:04	58.0	56.0	60.0	75	58.0	Fine	0.0
29-Jun-23	08:37	54.0	52.5	55.5	75	54.0	Fine	0.5
05-Jul-23	13:39	58.4	54.5	61.5	75	58.4	Fine	0.7
11-Jul-23	11:00	61.0	58.0	64.5	75	61.0	Sunny	0.5
18-Jul-23	08:39	53.6	51.5	55.0	75	53.6	Overcast	0.5
28-Jul-23	13:00	60.2	55.0	63.5	75	60.2	Fine	0.4
03-Aug-23	13:07	53.7	50.5	55.0	75	53.7	Fine	0.2
09-Aug-23	08:03	55.3	53.0	57.0	75	55.3	Sunny	0.5
15-Aug-23	13:05	54.3	52.0	55.5	75	54.3	Overcast	0.4
21-Aug-23	08:30	54.7	52.0	56.0	75	54.7	Fine	0.6

NMS 3 Hilton Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	14:42	66.7	64.0	68.5	75	66.7	Fine	0.5
10-May-23	10:15	62.2	60.0	64.0	75	62.2	Overcast	0.3
16-May-23	9:53	63.3	60.5	65.0	75	63.3	Fine	0.7
22-May-23	10:19	62.7	59.5	64.0	75	62.7	Fine	0.7
01-Jun-23	10:23	61.8	58.5	63.5	75	61.8	Fine	0.9
07-Jun-23	9:10	65.5	62.0	68.0	75	65.5	Overcast	0.4
13-Jun-23	10:38	67.4	64.5	69.5	75	67.4	Fine	0.6
19-Jun-23	8:35	66.0	63.0	68.0	75	66.0	Fine	0.0
29-Jun-23	17:07	66.4	63.5	68.5	75	66.4	Fine	0.4
05-Jul-23	9:56	63.1	61.0	65.5	75	63.1	Fine	0.3
11-Jul-23	8:36	63.0	60.0	64.0	75	63.0	Sunny	0.4
18-Jul-23	17:00	65.5	62.0	68.0	75	65.5	Overcast	0.6
28-Jul-23	11:11	61.8	59.5	64.5	75	61.8	Fine	0.5
03-Aug-23	9:56	63.1	61.0	65.5	75	63.1	Fine	0.3
09-Aug-23	16:18	64.2	62.5	67.5	75	64.2	Sunny	0.4
15-Aug-23	11:01	66.5	63.5	68.0	75	66.5	Overcast	1.3
21-Aug-23	16:12	66.4	63.5	67.0	75	66.4	Fine	0.5

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$\text{Corrected noise level (CNL)} = 10 \times \log \left[\left(\frac{\text{Measured noise level, Leq}}{10} \right) - \left(\frac{\text{Baseline noise level}}{10} \right) \right]$$

NMS 4 Tin Liu

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	15:53	62.6	60.5	64.0	75	62.6	Fine	0.2
10-May-23	11:30	62.0	60.5	64.5	75	62.0	Overcast	0.7
16-May-23	10:15	63.0	60.0	67.0	75	63.0	Fine	0.0
22-May-23	11:35	63.1	59.5	65.0	75	63.1	Fine	0.3
01-Jun-23	11:40	64.6	60.5	66.0	75	64.6	Fine	0.3
07-Jun-23	10:33	63.0	61.0	65.0	75	63.0	Overcast	0.5
13-Jun-23	10:02	62.3	60.5	64.0	75	62.3	Fine	0.4
19-Jun-23	10:46	62.6	61.0	64.0	75	62.6	Fine	0.0
29-Jun-23	9:16	63.1	60.5	65.5	75	63.1	Fine	0.2
05-Jul-23	14:15	63.4	61.0	65.5	75	63.4	Fine	0.7
11-Jul-23	10:47	64.3	61.5	68.0	75	64.3	Sunny	0.0
18-Jul-23	9:18	63.3	60.0	65.5	75	63.3	Overcast	0.3
28-Jul-23	13:36	62.3	60.0	64.0	75	62.3	Fine	0.4
03-Aug-23	9:10	65.0	62.0	66.0	75	65.0	Fine	0.2
09-Aug-23	8:46	64.8	61.0	67.0	75	64.8	Sunny	0.0
15-Aug-23	8:48	64.2	61.0	66.5	75	64.2	Overcast	0.2
21-Aug-23	9:12	65.8	61.0	67.0	75	65.8	Fine	0.4

NMS 5A Wai Wah Centre (Site Boundary)

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	14:03	67.3	65.5	68.5	75	67.3	Fine	0.4
10-May-23	9:15	67.6	62.5	69.5	75	67.6	Overcast	0.8
16-May-23	9:36	70.0	66.0	71.0	75	70.0	Fine	0.0
22-May-23	9:01	67.1	63.5	69.0	75	67.1	Fine	0.8
01-Jun-23	9:06	69.2	64.0	72.5	75	69.2	Fine	0.5
07-Jun-23	10:39	69.1	66.5	71.5	75	69.1	Overcast	0.4
13-Jun-23	11:16	70.3	68.5	73.5	75	70.3	Fine	0.4
19-Jun-23	9:09	68.5	66.0	70.0	75	68.5	Fine	0.0
29-Jun-23	16:25	68.8	65.5	70.0	75	68.8	Fine	0.6
05-Jul-23	9:18	68.4	63.0	71.5	75	68.4	Fine	0.5
11-Jul-23	9:10	62.7	61.0	64.0	75	62.7	Sunny	0.0
18-Jul-23	16:22	68.6	64.5	70.5	75	68.6	Overcast	0.4
28-Jul-23	09:54	66.3	64.5	69.0	75	66.3	Fine	0.7
03-Aug-23	10:18	68.7	65.0	70.0	75	68.7	Fine	0.5
09-Aug-23	15:42	69.7	66.5	71.5	75	69.7	Sunny	0.0
15-Aug-23	10:22	68.3	64.5	70.5	75	68.3	Overcast	0.6
21-Aug-23	15:31	69.7	66.5	72.0	75	69.7	Fine	0.5

NMS 6A Wai Wah Centre (Site Boundary)

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	8:35	72.7	70.5	74.5	75	72.7	Fine	0.6
10-May-23	8:23	69.4	65.5	72.5	75	69.4	Overcast	0.5
16-May-23	8:42	65.4	63.5	69.5	75	65.4	Fine	0.3
22-May-23	8:28	68.4	64.5	71.0	75	68.4	Fine	0.6
01-Jun-23	8:33	69.3	63.5	73.0	75	69.3	Fine	0.4
07-Jun-23	16:02	72.1	68.0	75.0	75	72.1	Overcast	0.3
13-Jun-23	13:03	69.7	67.5	72.0	75	69.7	Fine	0.7
19-Jun-23	9:41	68.0	65.0	70.0	75	68.0	Fine	0.0
29-Jun-23	15:47	74.1	71.5	76.0	75	74.1	Fine	0.6
05-Jul-23	8:45	66.9	63.0	70.5	75	66.9	Fine	0.4
11-Jul-23	9:42	71.9	70.0	73.5	75	71.9	Sunny	0.8
18-Jul-23	15:44	72.8	70.0	75.5	75	72.8	Overcast	0.3
28-Jul-23	09:13	67.9	64.5	71.5	75	67.9	Fine	0.5
03-Aug-23	9:42	74.6	72.0	76.5	75	74.6	Fine	0.6
09-Aug-23	15:03	73.6	69.5	75.5	75	73.6	Sunny	0.0
15-Aug-23	9:48	73.7	70.5	75.5	75	73.7	Overcast	0.6
21-Aug-23	14:54	71.8	68.5	74.5	75	71.8	Fine	0.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$Corrected\ noise\ level\ (CNL) = 10 \times \log \left[\left(10^{\frac{Measured\ noise\ level, L_{eq}}{10}} \right) - \left(10^{\frac{Baseline\ noise\ level}{10}} \right) \right]$$

NMS 7 Tin Liu

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	15:18	64.3	61.0	66.0	75	64.3	Fine	0.6
10-May-23	13:00	63.0	61.5	64.5	75	63.0	Overcast	0.7
16-May-23	9:44	64.5	61.0	66.0	75	64.5	Fine	0.2
22-May-23	13:00	63.7	60.5	66.0	75	63.7	Fine	0.2
01-Jun-23	13:04	64.3	60.0	65.5	75	64.3	Fine	0.4
07-Jun-23	11:10	64.3	62.0	66.0	75	64.3	Overcast	0.4
13-Jun-23	13:46	60.8	58.0	61.5	75	60.8	Fine	0.3
19-Jun-23	10:15	62.7	61.0	64.0	75	62.7	Fine	0.0
29-Jun-23	9:50	63.8	61.5	66.0	75	63.8	Fine	0.4
05-Jul-23	14:51	62.2	60.5	65.0	75	62.2	Fine	0.3
11-Jul-23	10:16	66.8	62.0	69.0	75	66.8	Sunny	0.0
18-Jul-23	9:55	64.9	62.5	66.5	75	64.9	Overcast	0.6
28-Jul-23	08:39	64.3	62.5	66.5	75	64.3	Fine	0.0
03-Aug-23	9:45	66.4	63.5	68.5	75	66.4	Fine	0.2
09-Aug-23	9:28	67.8	63.0	70.5	75	67.8	Sunny	0.0
15-Aug-23	9:36	65.7	63.5	68.5	75	65.7	Overcast	0.2
21-Aug-23	9:52	67.2	63.5	69.5	75	67.2	Fine	0.0

NMS 8 Shatin Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	8:54	62.2	59.5	65.5	75	62.2	Fine	0.5
11-May-23	8:00	66.0	65.0	69.0	75	66.0	Fine	0.6
17-May-23	8:44	62.7	59.0	65.0	75	62.7	Fine	0.6
23-May-23	8:00	67.0	65.0	69.0	75	67.0	Overcast	1.0
02-Jun-23	17:38	63.6	61.5	65.0	75	63.6	Fine	0.6
08-Jun-23	8:17	63.9	60.5	69.0	75	63.9	Overcast	0.2
14-Jun-23	8:30	65.1	61.5	66.0	75	65.1	Fine	0.0
20-Jun-23	8:49	61.8	58.5	65.0	75	61.8	Fine	0.7
30-Jun-23	8:44	63.7	57.5	66.0	75	63.7	Fine	0.4
06-Jul-23	9:00	62.4	61.5	65.0	75	62.4	Fine	0.5
12-Jul-23	8:58	61.1	59.5	63.5	75	61.1	Fine	0.4
19-Jul-23	8:30	64.8	61.0	66.5	75	64.8	Fine	0.4
29-Jul-23	08:47	62.1	60.0	64.5	75	62.1	Fine	0.8
04-Aug-23	8:34	64.8	62.0	66.5	75	64.8	Fine	0.3
10-Aug-23	17:34	66.3	64.0	68.3	75	66.3	Fine	0.0
16-Aug-23	8:30	66.4	64.5	69.0	75	66.4	Fine	0.6
22-Aug-23	17:57	67.2	65.0	69.5	75	67.2	Fine	0.4

NMS 9 Lek Yuen Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	10:02	64.8	62.5	68.5	75	64.8	Fine	0.8
11-May-23	9:08	67.0	65.0	70.0	75	67.0	Fine	0.0
17-May-23	9:51	65.9	63.0	69.0	75	65.9	Fine	0.4
23-May-23	9:07	68.0	66.0	71.0	75	68.0	Overcast	0.8
02-Jun-23	8:52	64.1	60.5	66.5	75	64.1	Fine	0.2
08-Jun-23	9:30	61.7	60.5	67.5	75	61.7	Overcast	0.4
14-Jun-23	9:49	64.8	59.5	66.0	75	64.8	Fine	0.0
20-Jun-23	9:56	68.4	62.5	71.0	75	68.4	Fine	0.7
30-Jun-23	9:51	68.4	65.0	71.5	75	68.4	Fine	0.2
06-Jul-23	10:11	67.2	63.5	70.5	75	67.2	Fine	0.6
12-Jul-23	10:09	65.3	62.5	68.5	75	65.3	Fine	0.4
19-Jul-23	9:50	64.6	60.0	66.0	75	64.6	Fine	0.4
29-Jul-23	09:54	67.6	60.5	70.0	75	67.6	Fine	0.7
04-Aug-23	9:47	64.7	59.5	66.5	75	64.7	Fine	0.4
10-Aug-23	8:30	67.3	65.0	69.5	75	67.3	Fine	0.0
16-Aug-23	9:48	67.8	65.0	70.0	75	67.8	Fine	0.6
22-Aug-23	8:30	68.3	65.0	70.5	75	68.3	Fine	0.2

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$\text{Corrected noise level (CNL)} = 10 \times \log \left[\left(10^{\frac{\text{Measured noise level, } L_{eq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 10A Shatin Tsung Tsin School

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-May-23	10:38	65.4	60.5	68.0	70	65.4	Fine	0.7
11-May-23	9:42	65.5	64.0	70.0	70	65.5	Fine	0.6
17-May-23	10:29	65.1	61.0	67.0	70	65.1	Fine	0.5
23-May-23	9:41	66.0	65.0	71.0	70	66.0	Overcast	1.4
02-Jun-23	9:28	64.0	61.0	65.5	70	64.0	Fine	0.3
08-Jun-23	10:11	63.2	59.5	66.0	65	63.2	Overcast	0.2
14-Jun-23	10:27	64.7	61.0	66.5	70	64.7	Fine	0.0
20-Jun-23	10:34	64.9	62.5	68.0	70	64.9	Fine	0.8
30-Jun-23	10:29	63.9	60.5	66.0	70	63.9	Fine	1.2
06-Jul-23	10:44	63.6	60.5	65.5	70	63.6	Fine	0.2
12-Jul-23	10:42	63.2	60.5	65.0	70	63.2	Fine	0.5
19-Jul-23	10:28	64.5	60.5	66.5	70	64.5	Fine	0.5
29-Jul-23	10:32	63.4	61.0	66.0	70	63.4	Fine	0.9
04-Aug-23	10:30	64.5	62.0	66.0	70	64.5	Fine	0.4
10-Aug-23	9:12	66.7	63.0	68.0	70	66.7	Fine	0.2
16-Aug-23	10:33	66.2	63.0	68.5	70	66.2	Fine	0.6
22-Aug-23	9:13	65.8	63.0	68.0	70	65.8	Fine	0.3

*Note: For Shatin Tsung Tsin School, 70 dB(A) noise level is set for school on normal days. The examination period was schedule on 8 June 2023. Hence, the daytime noise level changed from 70 to 65 dB(A).

NMS 11 Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-May-23	15:56	64.5	60.5	66.0	75	64.5	Fine	0.7
11-May-23	15:20	67.0	64.0	69.0	75	67.0	Fine	0.0
17-May-23	15:57	63.9	59.5	65.5	75	63.9	Fine	0.4
23-May-23	15:18	68.0	66.0	70.0	75	68.0	Overcast	0.8
02-Jun-23	15:38	61.9	58.0	63.0	75	61.9	Fine	0.3
08-Jun-23	16:37	60.7	57.5	64.0	75	60.7	Overcast	0.4
14-Jun-23	16:07	60.1	59.0	61.0	75	60.1	Fine	0.3
20-Jun-23	16:00	62.5	58.5	65.5	75	62.5	Fine	0.7
30-Jun-23	15:57	62.5	61.5	66.5	75	62.5	Fine	0.8
06-Jul-23	15:55	62.3	59.5	66.0	75	62.3	Fine	0.4
12-Jul-23	15:58	62.7	60.0	65.0	75	62.7	Fine	0.6
19-Jul-23	16:06	60.4	59.0	61.5	75	60.4	Fine	0.4
29-Jul-23	15:56	62.4	59.5	65.5	75	62.4	Fine	0.7
04-Aug-23	15:55	62.3	59.5	66.0	75	62.3	Fine	0.4
10-Aug-23	15:36	65.5	62.0	68.0	75	65.5	Fine	0.2
16-Aug-23	15:58	64.7	62.5	67.5	75	64.7	Fine	0.6
22-Aug-23	15:56	65.5	62.5	68.0	75	65.5	Fine	0.2

NMS 12 SKH Holy Spirit Primary School

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-May-23	11:12	62.1	57.5	65.0	70	62.1	Fine	0.5
11-May-23	10:17	63.0	60.0	66.0	70	63.0	Fine	0.5
17-May-23	11:03	60.7	58.0	64.0	70	60.7	Fine	0.8
23-May-23	10:19	64.0	63.0	68.0	70	64.0	Overcast	0.8
02-Jun-23	10:10	62.3	61.0	63.5	65	62.3	Fine	0.2
08-Jun-23	10:55	62.9	60.0	64.0	70	62.9	Overcast	0.3
14-Jun-23	11:07	63.9	60.5	66.0	70	63.9	Fine	0.5
20-Jun-23	11:08	62.4	59.5	65.5	70	62.4	Fine	0.9
30-Jun-23	11:03	63.1	59.5	65.5	70	63.1	Fine	0.7
06-Jul-23	11:16	61.8	58.5	64.0	65	61.8	Fine	0.3
12-Jul-23	11:14	62.5	59.5	64.5	70	62.5	Fine	0.3
19-Jul-23	11:06	64.1	60.0	66.0	70	64.1	Fine	0.5
29-Jul-23	11:06	63.9	60.5	65.5	70	63.9	Fine	0.7
04-Aug-23	11:12	63.6	60.0	65.5	70	63.6	Fine	0.2
10-Aug-23	9:56	64.7	63.5	68.0	70	64.7	Fine	0.0
16-Aug-23	11:14	66.3	63.5	69.0	70	66.3	Fine	0.6
22-Aug-23	9:48	66.7	63.0	69.0	70	66.7	Fine	0.2

*Note: For SKH Holy Spirit Primary School, 70 dB(A) noise level is set for school on normal days. The examination was scheduled on 2 June 2023 and 6 July 2023. Hence, the daytime noise level changed from 70 to 65 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$Corrected\ noise\ level\ (CNL) = 10 \times \log \left[\left(10^{\frac{Measured\ noise\ level, L_{eq}}{10}} \right) - \left(10^{\frac{Baseline\ noise\ level}{10}} \right) \right]$$

NMS 13 Lek Yuen Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	11:46	61.3	58.5	64.5	75	61.3	Fine	0.5
11-May-23	10:50	65.0	63.0	69.0	75	65.0	Fine	0.6
17-May-23	11:36	63.4	60.0	65.0	75	63.4	Fine	0.7
23-May-23	10:52	67.0	65.0	70.0	75	67.0	Overcast	0.8
02-Jun-23	10:48	60.0	56.5	61.5	75	60.0	Fine	0.2
08-Jun-23	11:34	61.2	59.0	64.0	75	61.2	Overcast	0.2
14-Jun-23	13:00	60.8	57.0	62.5	75	60.8	Fine	0.2
20-Jun-23	11:41	65.7	59.5	68.5	75	65.7	Fine	0.6
30-Jun-23	11:36	64.4	61.5	66.5	75	64.4	Fine	0.9
06-Jul-23	11:48	65.2	59.5	67.5	75	65.2	Fine	0.3
12-Jul-23	11:46	63.7	59.5	65.5	75	63.7	Fine	0.3
19-Jul-23	11:47	61.2	57.5	63.0	75	61.2	Fine	0.4
29-Jul-23	11:39	65.7	61.0	68.5	75	65.7	Fine	0.8
04-Aug-23	13:09	61.3	58.0	63.0	75	61.3	Fine	0.0
10-Aug-23	10:41	68.2	65.5	71.0	75	68.2	Fine	0.2
16-Aug-23	13:12	68.2	66.0	71.5	75	68.2	Fine	0.6
22-Aug-23	10:26	68.2	66.5	71.5	75	68.2	Fine	0.2

NMS 14 Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	15:21	65.3	61.5	69.5	75	65.3	Fine	0.8
11-May-23	15:20	67.0	64.0	69.0	75	67.0	Fine	0.0
17-May-23	15:23	64.6	62.0	66.5	75	64.6	Fine	0.7
23-May-23	14:46	68.0	66.0	69.0	75	68.0	Overcast	0.6
02-Jun-23	14:59	62.3	58.5	64.5	75	62.3	Fine	0.2
08-Jun-23	15:53	61.4	58.5	63.0	75	61.4	Overcast	0.0
14-Jun-23	15:30	62.3	58.5	64.0	75	62.3	Fine	0.3
20-Jun-23	15:25	66.8	64.0	67.5	75	66.8	Fine	0.8
30-Jun-23	15:23	67.2	60.5	69.0	75	67.2	Fine	0.5
06-Jul-23	15:20	65.4	61.0	69.0	75	65.4	Fine	0.3
12-Jul-23	15:24	62.4	60.5	64.5	75	62.4	Fine	0.4
19-Jul-23	15:30	62.6	59.0	64.0	75	62.6	Fine	0.4
29-Jul-23	15:22	62.1	60.0	64.5	75	62.1	Fine	0.7
04-Aug-23	15:20	65.4	61.0	69.0	75	65.4	Fine	0.3
10-Aug-23	14:58	59.4	57.5	61.0	75	59.4	Fine	0.0
16-Aug-23	15:24	59.7	57.0	67.5	75	59.7	Fine	0.6
22-Aug-23	15:08	59.2	57.0	61.5	75	59.2	Fine	0.2

NMS 15 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	10:58	61.2	58.0	63.5	75	61.2	Fine	0.7
10-May-23	14:10	61.3	58.5	63.5	75	61.3	Overcast	0.3
16-May-23	10:39	61.8	59.5	63.5	75	61.8	Fine	0.5
22-May-23	14:11	60.9	58.0	62.5	75	60.9	Fine	0.6
01-Jun-23	14:15	60.1	59.0	63.5	75	60.1	Fine	0.6
07-Jun-23	14:00	60.1	57.0	61.5	75	60.1	Overcast	0.4
13-Jun-23	14:59	53.2	51.5	55.5	75	53.2	Fine	0.6
19-Jun-23	13:37	62.3	59.5	63.5	75	62.3	Fine	0.0
29-Jun-23	13:48	62.5	60.0	63.5	75	62.5	Fine	0.5
05-Jul-23	10:43	62.7	60.0	64.0	75	62.7	Fine	0.5
11-Jul-23	13:41	64.8	63.0	68.0	75	64.8	Sunny	0.5
18-Jul-23	13:49	61.4	59.0	63.5	75	61.4	Overcast	0.5
28-Jul-23	10:03	56.7	53.5	58.5	75	56.7	Fine	0.5
03-Aug-23	10:30	64.8	61.0	65.5	75	64.8	Fine	0.2
09-Aug-23	13:00	63.3	59.5	65.0	75	63.3	Sunny	0.5
15-Aug-23	10:52	63.8	60.0	63.5	75	63.8	Overcast	0.2
21-Aug-23	13:00	63.1	59.5	65.0	75	63.1	Fine	0.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$\text{Corrected noise level (CNL)} = 10 \times \log \left[\left(10^{\frac{\text{Measured noise level, } L_{eq}}{10}} - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right) \right]$$

NMS 16 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
04-May-23	11:34	63.2	60.0	65.5	75	63.2	Fine	0.4
10-May-23	15:14	60.4	57.0	62.0	75	60.4	Overcast	0.3
16-May-23	11:45	60.8	57.5	63.0	75	60.8	Fine	0.6
22-May-23	15:17	61.3	59.0	63.5	75	61.3	Fine	0.5
01-Jun-23	15:21	62.4	58.0	64.0	75	62.4	Fine	0.7
07-Jun-23	14:38	61.7	58.0	63.5	75	61.7	Overcast	0.4
13-Jun-23	15:38	55.3	52.5	57.5	75	55.3	Fine	0.6
19-Jun-23	14:08	61.4	59.0	63.5	75	61.4	Fine	0.0
29-Jun-23	14:24	62.9	59.5	64.0	75	62.9	Fine	0.4
05-Jul-23	11:48	60.9	58.5	62.5	75	60.9	Fine	0.7
11-Jul-23	14:12	64.5	63.0	66.0	75	64.5	Sunny	0.0
18-Jul-23	14:25	62.2	60.0	63.5	75	62.2	Overcast	0.2
28-Jul-23	10:44	54.8	52.5	57.0	75	54.8	Fine	0.6
03-Aug-23	11:08	66.2	63.0	68.0	75	66.2	Fine	0.2
09-Aug-23	13:41	62.4	59.0	64.5	75	62.4	Sunny	0.0
15-Aug-23	11:31	61.3	58.0	64.0	75	61.3	Overcast	0.2
21-Aug-23	13:34	61.2	58.0	67.5	75	61.2	Fine	0.2

NMS 17 Shatin Pui Ying College

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
05-May-23	13:00	66.3	62.0	68.0	65	66.3 [^]	Fine	0.8
11-May-23	13:00	67.2	65.0	69.0	65	56.6	Fine	0.6
17-May-23	13:00	65.3	63.5	67.5	70	65.3	Fine	0.5
23-May-23	13:00	67.0	65.0	70.0	70	67.0	Overcast	1.0
02-Jun-23	11:28	63.1	60.5	65.0	70	63.1	Fine	0.4
08-Jun-23	13:12	62.8	60.5	66.0	65	62.8	Overcast	0.2
14-Jun-23	13:00	63.3	60.5	65.5	65	63.3	Fine	0.1
20-Jun-23	13:00	66.1	62.5	68.5	70	66.1	Fine	0.8
30-Jun-23	13:00	64.9	61.5	67.0	70	64.9	Fine	0.5
06-Jul-23	13:00	64.9	62.0	67.5	70	64.9	Fine	0.2
12-Jul-23	13:00	63.3	60.5	66.5	70	63.3	Fine	0.5
19-Jul-23	13:00	62.9	60.0	65.0	70	62.9	Fine	0.4
29-Jul-23	13:00	63.0	61.5	65.5	70	63.0	Fine	0.6
04-Aug-23	13:58	61.9	59.0	65.5	70	61.9	Fine	0.5
10-Aug-23	13:00	68.1	64.5	71.0	70	68.1	Fine	0.0
16-Aug-23	14:00	66.8	64.5	69.0	70	66.8	Fine	0.6
22-Aug-23	13:00	68.7	65.0	70.0	70	68.7	Fine	0.2

*Note: For Shatin Pui Ying College, 70 dB(A) noise level is set for school on normal days. The DSE was schedule on 5, 11 May 2023 and examination was scheduled on 8, 14 June 2023. Hence, the daytime noise level changed from 70 to 65 dB(A).

[^]Note: The noise level recorded on 5 May 2023 was below the baseline level, it is not considered as an exceedance.

NMS 18 Ha Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
		Unit: dB(A) 30 Mins						
04-May-23	13:10	62.0	60.5	63.5	75	62.0	Fine	0.0
10-May-23	14:42	61.1	57.5	62.5	75	61.1	Overcast	0.4
16-May-23	11:13	60.4	58.0	63.5	75	60.4	Fine	0.5
22-May-23	14:45	61.5	58.5	63.0	75	61.5	Fine	0.9
01-Jun-23	14:49	62.7	59.0	64.5	75	62.7	Fine	0.8
07-Jun-23	15:16	61.5	60.0	63.5	75	61.5	Overcast	0.4
13-Jun-23	16:14	54.4	51.5	56.5	75	54.4	Fine	0.5
19-Jun-23	14:39	61.0	59.0	63.0	75	61.0	Fine	0.0
29-Jun-23	14:58	62.3	60.0	64.0	75	62.3	Fine	0.2
05-Jul-23	11:16	61.4	59.0	63.5	75	61.4	Fine	0.4
11-Jul-23	14:43	66.0	65.5	67.0	75	66.0	Sunny	0.0
18-Jul-23	14:59	63.1	60.0	65.5	75	63.1	Overcast	0.3
28-Jul-23	11:21	59.6	56.5	61.5	75	59.6	Fine	0.4
03-Aug-23	11:45	65.1	61.0	66.5	75	65.1	Fine	0.2
09-Aug-23	14:24	63.0	58.0	64.0	75	63.0	Sunny	0.0
15-Aug-23	13:00	67.4	59.0	64.5	75	67.4	Overcast	0.2
21-Aug-23	14:13	63.4	58.0	65.0	75	63.4	Fine	0.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$Corrected\ noise\ level\ (CNL) = 10 \times \log \left[\left(10^{\frac{Measured\ noise\ level, L_{eq}}{10}} - \left(10^{\frac{Baseline\ noise\ level}{10}} \right) \right) \right]$$

NMS 19 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	13:34	61.4	59.5	63.5	75	61.4	Fine	0.7
11-May-23	13:34	66.0	65.0	68.0	75	66.0	Fine	0.0
17-May-23	13:35	62.9	59.0	64.5	75	62.9	Fine	0.8
23-May-23	13:34	67.0	65.0	70.0	75	67.0	Overcast	0.7
02-Jun-23	13:06	64.5	60.5	66.5	75	64.5	Fine	0.5
08-Jun-23	13:51	64.7	62.0	66.5	75	64.7	Overcast	0.2
14-Jun-23	13:36	63.3	61.0	65.0	75	63.3	Fine	0.3
20-Jun-23	13:36	64.3	60.0	66.5	75	64.3	Fine	0.7
30-Jun-23	13:35	62.7	59.5	65.0	75	62.7	Fine	0.6
06-Jul-23	13:33	62.6	59.5	64.5	75	62.6	Fine	0.6
12-Jul-23	13:36	64.7	60.0	67.5	75	64.7	Fine	0.4
19-Jul-23	13:37	63.5	60.5	65.5	75	63.5	Fine	0.4
29-Jul-23	13:34	62.2	59.5	64.5	75	62.2	Fine	0.8
04-Aug-23	13:33	62.6	59.5	64.5	75	62.6	Fine	0.6
10-Aug-23	13:42	67.4	66.0	68.0	75	67.4	Fine	0.0
16-Aug-23	13:36	68.2	59.0	65.5	75	68.2	Fine	0.6
22-Aug-23	13:42	68.7	66.5	71.0	75	68.7	Fine	0.2

NMS 20 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	14:06	66.3	63.5	67.5	75	66.3	Fine	0.6
11-May-23	14:05	66.5	64.0	69.0	75	66.5	Fine	0.0
17-May-23	14:08	65.8	62.0	68.0	75	65.8	Fine	0.9
23-May-23	14:05	67.0	65.0	70.0	75	67.0	Overcast	0.9
02-Jun-23	13:41	62.7	59.0	64.0	75	62.7	Fine	0.4
08-Jun-23	14:29	63.1	60.5	67.0	75	63.1	Overcast	0.3
14-Jun-23	14:12	64.0	61.5	66.0	75	64.0	Fine	0.4
20-Jun-23	14:09	64.7	61.0	67.5	75	64.7	Fine	0.8
30-Jun-23	14:08	63.9	60.5	67.5	75	63.9	Fine	0.6
06-Jul-23	14:05	65.1	63.5	69.5	75	65.1	Fine	0.2
12-Jul-23	14:09	64.4	60.5	67.0	75	64.4	Fine	0.5
19-Jul-23	14:13	64.2	61.5	65.5	75	64.2	Fine	0.5
29-Jul-23	14:09	62.8	59.5	65.0	75	62.8	Fine	0.7
04-Aug-23	14:05	65.1	63.5	69.5	75	65.1	Fine	0.2
10-Aug-23	14:21	64.3	59.5	66.0	75	64.3	Fine	0.2
16-Aug-23	14:09	63.4	59.0	65.5	75	63.4	Fine	0.6
22-Aug-23	14:28	62.8	57.5	64.0	75	62.8	Fine	0.2

NMS 23 Pai Tau

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	10:20	63.1	61.0	64.5	75	63.1	Fine	0.4
10-May-23	13:33	63.9	60.0	65.5	75	63.9	Overcast	0.6
16-May-23	9:13	65.0	61.0	67.0	75	65.0	Fine	0.0
22-May-23	13:35	63.6	61.0	65.5	75	63.6	Fine	0.9
01-Jun-23	13:39	63.8	59.5	65.0	75	63.8	Fine	0.5
07-Jun-23	11:45	63.2	60.5	65.0	75	63.2	Overcast	0.4
13-Jun-23	14:21	63.1	60.5	65.0	75	63.1	Fine	0.6
19-Jun-23	13:00	65.0	62.0	67.0	75	65.0	Fine	0.0
29-Jun-23	13:04	61.5	58.5	63.5	75	61.5	Fine	0.4
05-Jul-23	15:25	65.4	60.5	68.5	75	65.4	Fine	0.8
11-Jul-23	13:00	67.5	65.0	70.5	75	67.5	Sunny	0.0
18-Jul-23	13:10	62.6	59.5	64.0	75	62.6	Overcast	0.2
28-Jul-23	09:18	64.2	62.5	66.0	75	64.2	Fine	0.6
03-Aug-23	12:35	64.0	61.5	65.5	75	64.0	Fine	0.2
09-Aug-23	10:21	62.4	60.0	65.0	75	62.4	Sunny	0.0
15-Aug-23	10:13	63.2	60.5	65.5	75	63.2	Overcast	0.2
21-Aug-23	10:32	63.2	60.5	66.0	75	63.2	Fine	0.3

NMS 24 Shatin Plaza

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	9:27	63.7	61.5	66.0	75	63.7	Fine	0.8
11-May-23	9:15	63.2	60.5	64.5	75	63.2	Fine	0.3
17-May-23	9:16	64.2	60.5	66.5	75	64.2	Fine	0.9
23-May-23	9:37	62.2	58.5	65.0	75	62.2	Overcast	0.6
02-Jun-23	17:02	62.7	60.0	64.5	75	62.7	Fine	0.6
08-Jun-23	8:54	61.4	58.0	64.0	75	61.4	Overcast	0.3
14-Jun-23	9:04	63.4	60.0	65.5	75	63.4	Fine	0.0
20-Jun-23	9:21	63.2	60.0	65.5	75	63.2	Fine	0.8
30-Jun-23	9:16	62.4	58.0	65.5	75	62.4	Fine	1.2
06-Jul-23	9:33	63.7	59.5	65.5	75	63.7	Fine	0.5
12-Jul-23	9:31	64.8	59.5	66.5	75	64.8	Fine	0.3
19-Jul-23	9:03	64.1	60.5	65.5	75	64.1	Fine	0.5
29-Jul-23	9:19	62.7	60.0	65.5	75	62.7	Fine	0.8
04-Aug-23	9:08	63.3	60.5	65.0	75	63.3	Fine	0.0
10-Aug-23	16:52	69.3	66.0	72.5	75	69.3	Fine	0.0
16-Aug-23	9:13	67.2	65.5	70.0	75	67.2	Fine	0.6
22-Aug-23	17:16	68.8	65.5	70.5	75	68.8	Fine	0.2

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$Corrected\ noise\ level\ (CNL) = 10 \times \log \left[\left(10^{\frac{Measured\ noise\ level, L_{eq}}{10}} \right) - \left(10^{\frac{Baseline\ noise\ level}{10}} \right) \right]$$

NMS 25A Sheung Wo Che

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	16:30	68.1	65.0	70.5	75	68.1	Fine	0.5
11-May-23	15:54	69.0	65.0	71.0	75	69.0	Fine	0.4
17-May-23	16:53	69.0	64.5	71.5	75	69.0	Fine	0.6
23-May-23	15:52	69.0	67.0	72.0	75	69.0	Overcast	0.6
02-Jun-23	16:14	63.1	60.0	65.5	75	63.1	Fine	0.2
08-Jun-23	17:21	64.1	61.5	67.5	75	64.1	Overcast	0.4
14-Jun-23	10:43	65.4	61.0	67.5	75	65.4	Fine	0.4
20-Jun-23	16:36	67.4	63.0	69.5	75	67.4	Fine	0.8
30-Jun-23	16:33	68.3	63.5	69.5	75	68.3	Fine	0.5
06-Jul-23	16:28	66.9	64.0	70.0	75	66.9	Fine	0.3
12-Jul-23	16:34	63.1	60.5	65.5	75	63.1	Fine	0.6
19-Jul-23	16:42	66.1	61.0	68.0	75	66.1	Fine	0.4
29-Jul-23	16:32	64.3	60.5	68.5	75	64.3	Fine	0.8
04-Aug-23	16:28	66.9	64.0	70.0	75	66.9	Fine	0.3
10-Aug-23	16:13	67.1	65.0	69.5	75	67.1	Fine	0.0
16-Aug-23	16:30	67.8	64.5	69.0	75	67.8	Fine	0.6
22-Aug-23	16:38	66.2	63.0	69.5	75	66.2	Fine	0.2

NMS 26 Wo Che Estate

Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
05-May-23	14:42	66.9	63.5	68.5	75	66.9	Fine	0.6
11-May-23	11:29	69.0	66.0	71.0	75	69.0	Fine	0.0
17-May-23	14:45	64.4	61.5	67.0	75	64.4	Fine	0.6
23-May-23	11:30	71.0	68.0	73.0	75	71.0	Overcast	0.0
02-Jun-23	14:20	70.6	67.0	71.5	75	70.6	Fine	0.5
08-Jun-23	15:10	70.4	64.5	72.0	75	70.4	Overcast	0.2
14-Jun-23	14:49	70.2	67.5	72.0	75	70.2	Fine	0.0
20-Jun-23	14:47	65.2	63.5	68.5	75	65.2	Fine	0.9
30-Jun-23	14:45	62.8	62.0	65.5	75	62.8	Fine	0.8
06-Jul-23	14:41	66.2	63.5	68.5	75	66.2	Fine	0.3
12-Jul-23	14:46	67.9	62.5	69.5	75	67.9	Fine	0.8
19-Jul-23	14:50	70.6	67.0	72.5	75	70.6	Fine	0.4
29-Jul-23	14:47	66.9	62.5	69.5	75	66.9	Fine	0.8
04-Aug-23	14:41	66.2	63.5	68.5	75	66.2	Fine	0.3
10-Aug-23	11:18	68.4	64.0	71.0	75	68.4	Fine	0.0
16-Aug-23	14:46	68.7	64.0	70.5	75	68.7	Fine	0.6
22-Aug-23	11:08	68.3	64.5	71.0	75	68.3	Fine	0.2

NMS 27 Jockey Club Ti-I College







Date	Start Time	Measured Noise Level			Limit Level	Construction Noise Level	Weather	Wind Speed (m/s)
		L _{eq}	L ₉₀	L ₁₀				
Unit: dB(A) 30 Mins								
04-May-23	09:28	63.4	60.0	65.0	70	63.4	Fine	0.6
10-May-23	16:21	66.5	64.0	69.0	70	66.5	Overcast	0.3
16-May-23	13:00	68.6	63.5	70.5	65	68.6^	Fine	0.8
22-May-23	16:20	67.2	64.5	70.0	70	67.2	Fine	0.5
01-Jun-23	16:25	66.4	63.5	69.5	70	66.4	Fine	0.4
07-Jun-23	13:00	63.9	61.0	66.5	70	63.9	Overcast	0.3
13-Jun-23	16:58	63.6	62.0	66.5	70	63.6	Fine	0.6
19-Jun-23	15:05	63.0	60.0	65.0	70	63.0	Fine	0.0
29-Jun-23	10:48	61.7	59.0	63.5	70	61.7	Fine	0.2
05-Jul-23	16:22	67.1	64.5	70.5	70	67.1	Fine	0.8
11-Jul-23	15:33	65.0	62.0	67.0	70	65.0	Sunny	0.6
18-Jul-23	10:07	62.9	59.5	64.0	70	62.9	Overcast	0.8
28-Jul-23	13:06	65.6	63.0	68.0	70	65.6	Fine	0.0
03-Aug-23	08:46	62.0	60.5	63.0	70	62.0	Fine	0.4
09-Aug-23	10:56	64.7	61.0	67.5	70	64.7	Sunny	0.0
15-Aug-23	08:52	63.8	60.0	65.0	70	63.8	Overcast	0.7
21-Aug-23	11:12	65.7	61.0	67.5	70	65.7	Fine	0.2







*Note: For Jockey Club Ti-I College, 70 dB(A) noise level is set for school on normal days. The DSE was scheduled on 16 May 2023. Hence, the daytime noise level changed from 70 to 65 dB(A).







^Note: The noise level recorded on 16 May 2023 was below the baseline level, it is not considered as an exceedance.








If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$Corrected\ noise\ level\ (CNL) = 10 \times \log \left[\left(10^{\frac{Measured\ noise\ level, L_{eq}}{10}} \right) - \left(10^{\frac{Baseline\ noise\ level}{10}} \right) \right]$$

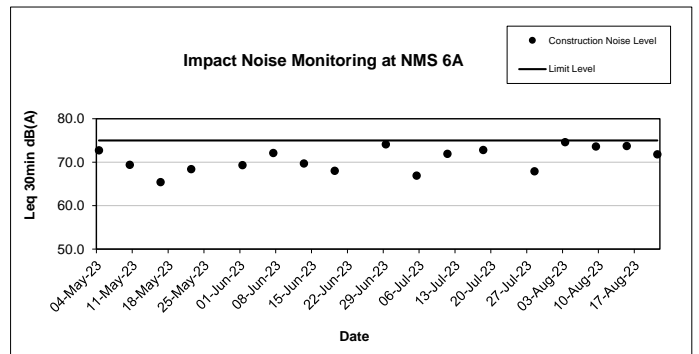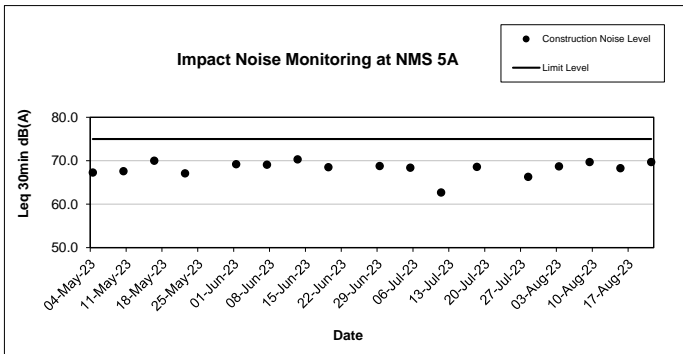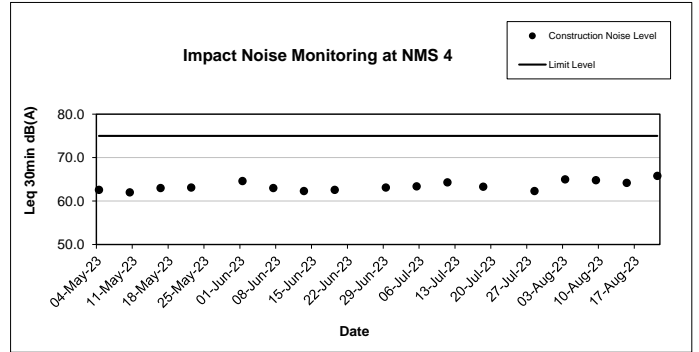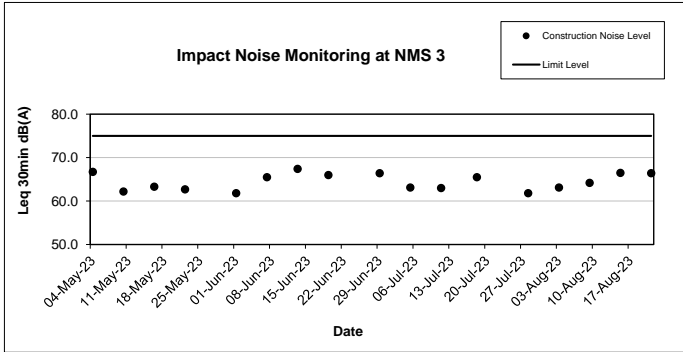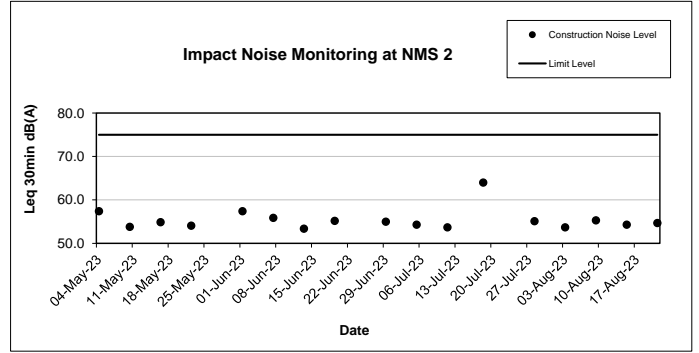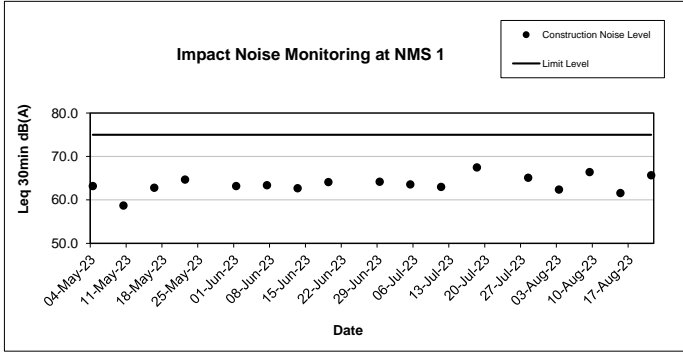

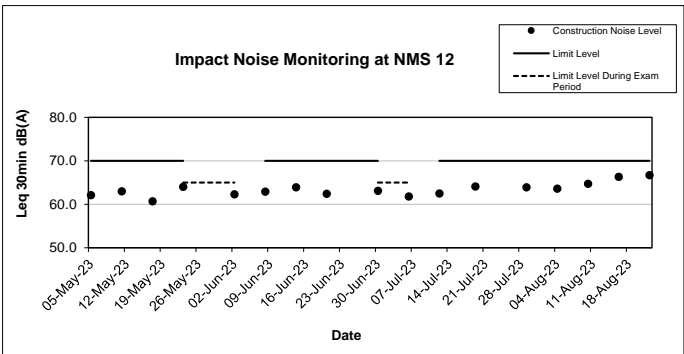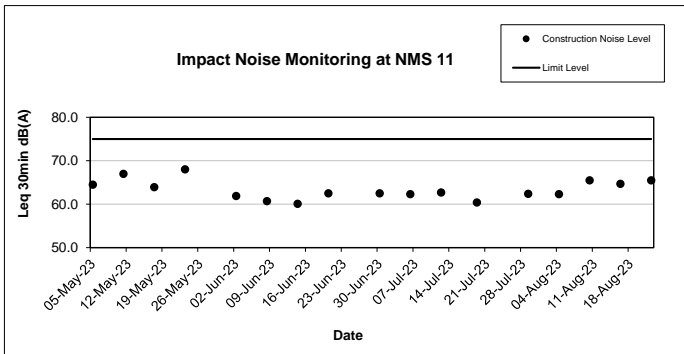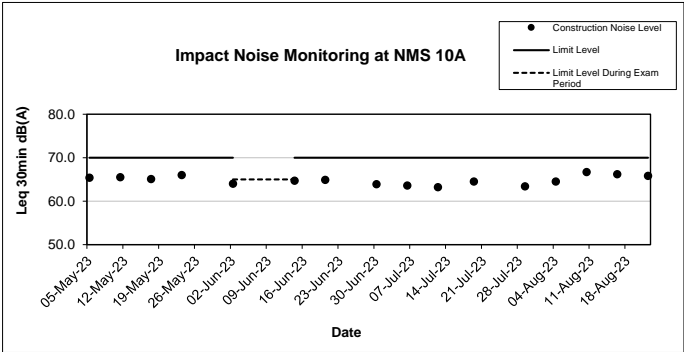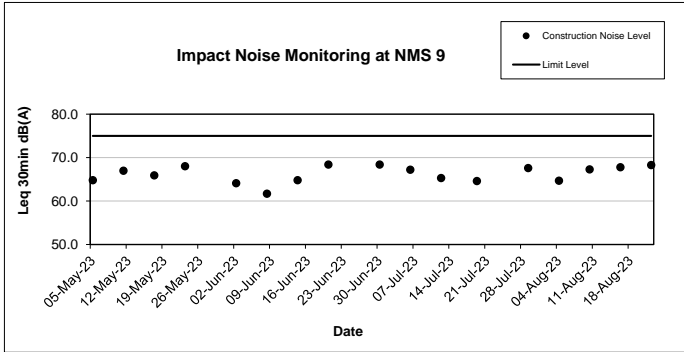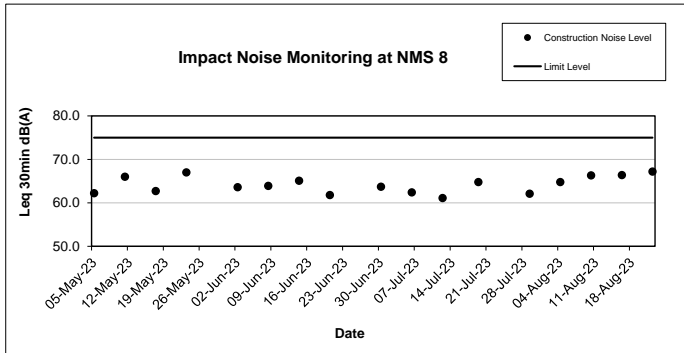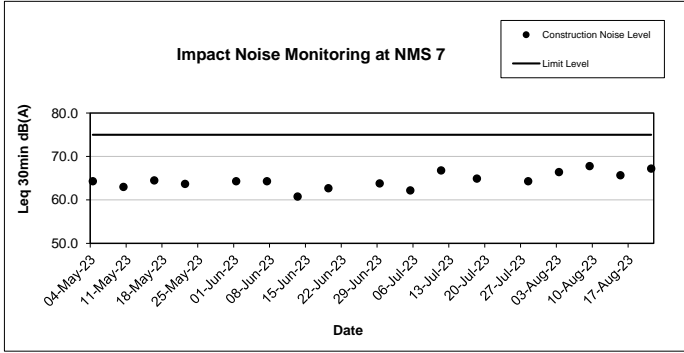

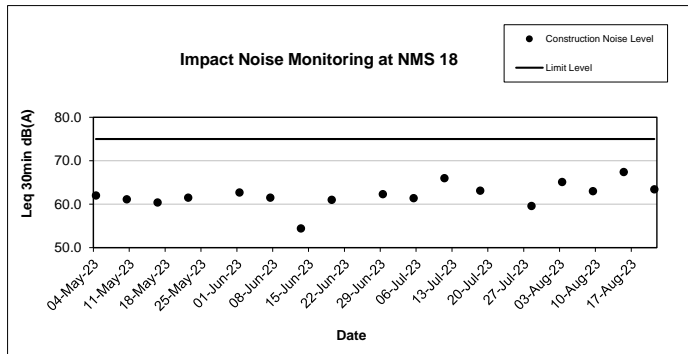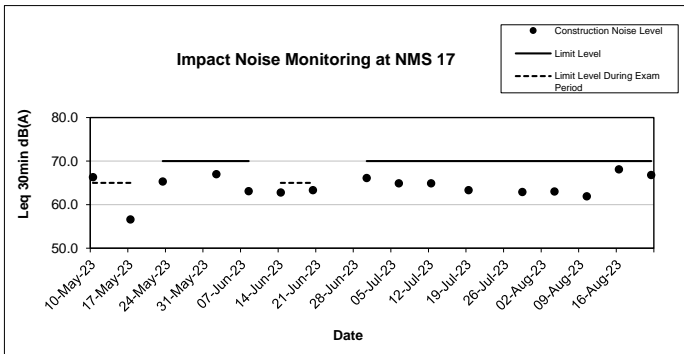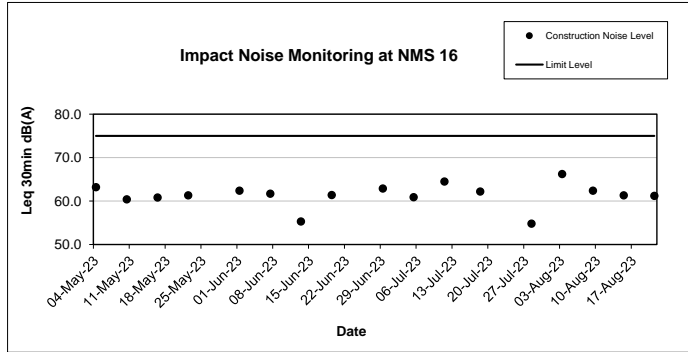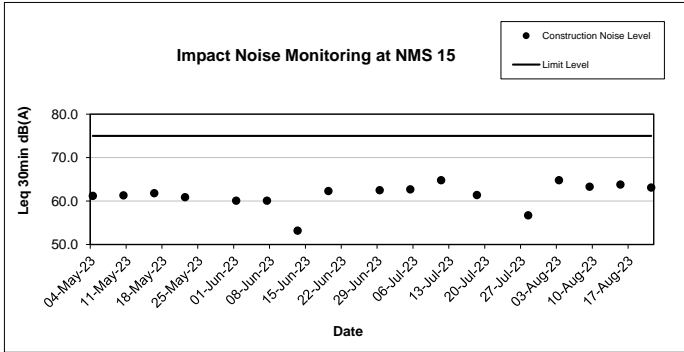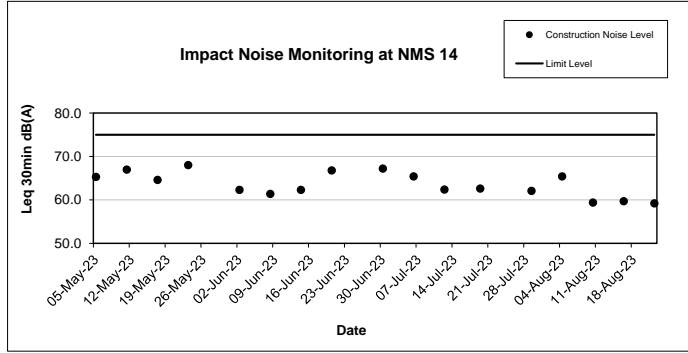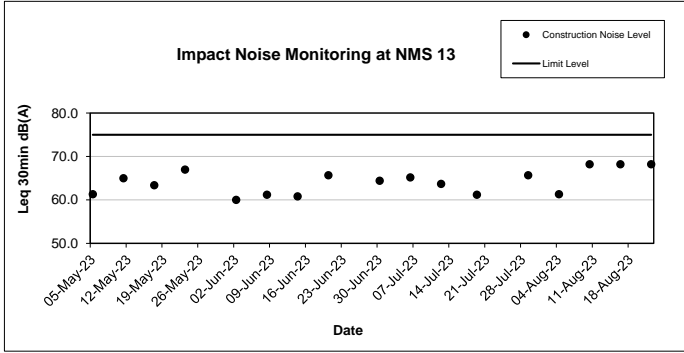

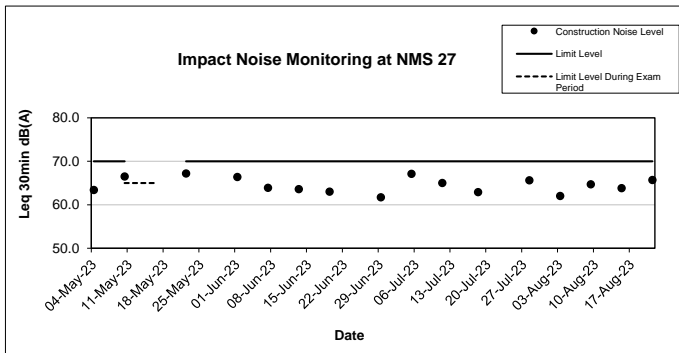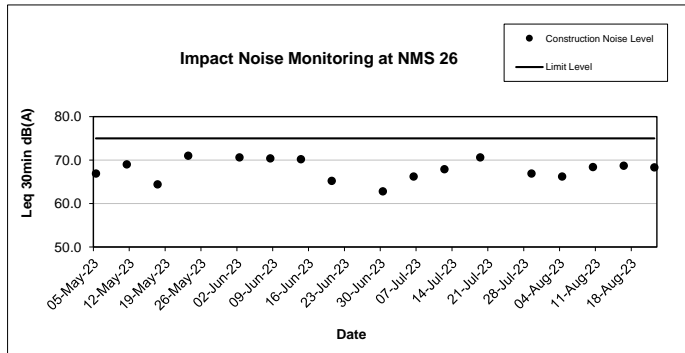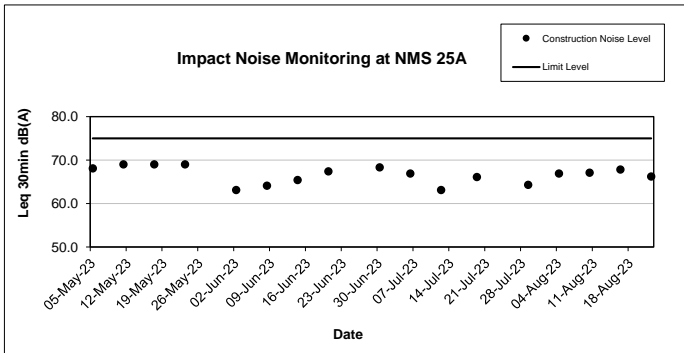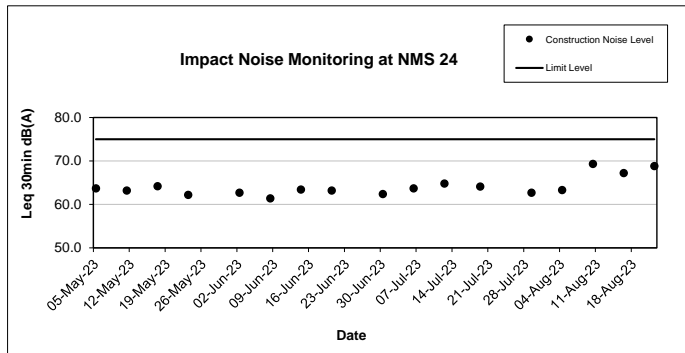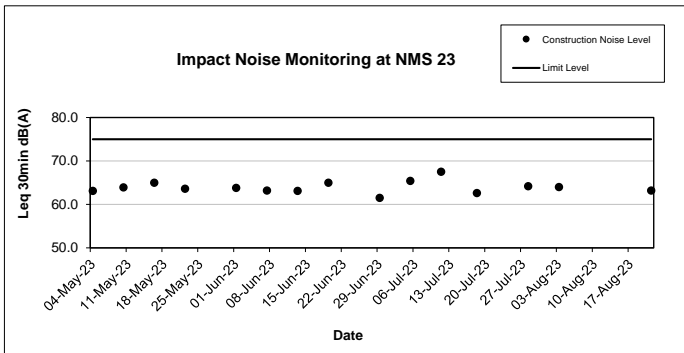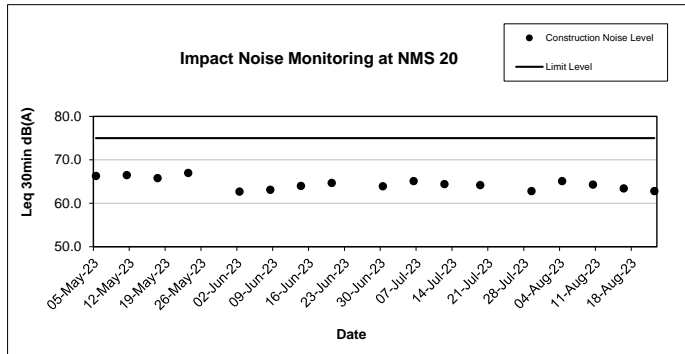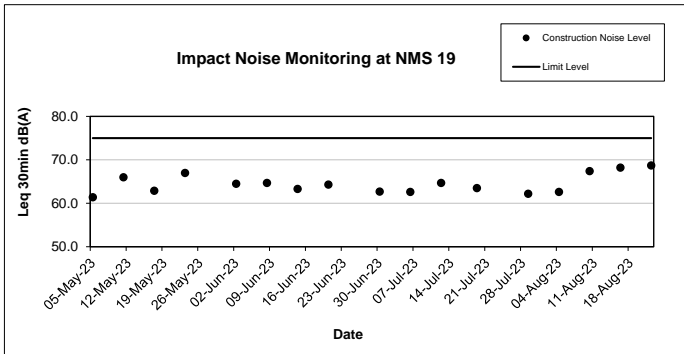

Night Time Noise Monitoring Result for NOD 03-2018 Road Widening and Retrofitting Noise Barriers on Tai Po Road (Sha Tin Section)

NMS 1 Scenery Court

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	00:20	58.1	61.4	52.8 - 66.3	55	Measured Noise Level<Baseline	Fine	0.2
09-May-23	23:03	59.5				Measured Noise Level<Baseline	Fine	0.3
19-May-23	01:02	58.1				Measured Noise Level<Baseline	Fine	0.2
23-May-23	23:01	59.0				Measured Noise Level<Baseline	Fine	0.2
02-Jun-23	01:00	58.4				Measured Noise Level<Baseline	Fine	0.2
06-Jun-23	23:02	58.9				Measured Noise Level<Baseline	Fine	0.3
16-Jun-23	00:42	58.2				Measured Noise Level<Baseline	Fine	0.0
20-Jun-23	23:11	59.5				Measured Noise Level<Baseline	Fine	0.5
29-Jun-23	23:46	58.3				Measured Noise Level<Baseline	Overcast	0.5
04-Jul-23	23:04	58.8				Measured Noise Level<Baseline	Fine	0.2
14-Jul-23	03:17	57.8				Measured Noise Level<Baseline	Fine	0.2
18-Jul-23	03:00	58.2				Measured Noise Level<Baseline	Fine	0.2
28-Jul-23	01:15	58.3				Measured Noise Level<Baseline	Fine	0.2
01-Aug-23	23:12	58.2				Measured Noise Level<Baseline	Fine	0.2
11-Aug-23	01:05	58.9				Measured Noise Level<Baseline	Fine	0.2
15-Aug-23	23:01	58.7				Measured Noise Level<Baseline	Fine	0.2
25-Aug-23	01:22	58.7				Measured Noise Level<Baseline	Fine	0.0
29-Aug-23	23:08	59.2				Measured Noise Level<Baseline	Fine	0.3

NMS 2 Villa Le Parc

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:00	51.8	49.7	40.1 - 58.2	55	Measured Noise Level<Limit Level	Fine	0.7
09-May-23	23:04	52.6				Measured Noise Level<Limit Level	Fine	0.5
18-May-23	23:00	52.1				Measured Noise Level<Limit Level	Fine	0.7
23-May-23	23:06	52.5				Measured Noise Level<Limit Level	Fine	0.7
01-Jun-23	23:00	53.3				Measured Noise Level<Limit Level	Fine	0.8
06-Jun-23	23:04	52.7				Measured Noise Level<Limit Level	Fine	0.4
15-Jun-23	23:00	53.3				Measured Noise Level<Limit Level	Fine	0.6
20-Jun-23	23:06	53.6				Measured Noise Level<Limit Level	Fine	0.3
29-Jun-23	23:14	52.0				Measured Noise Level<Limit Level	Overcast	0.4
04-Jul-23	23:06	53.4				Measured Noise Level<Limit Level	Fine	0.7
13-Jul-23	23:02	51.7				Measured Noise Level<Limit Level	Fine	0.2
18-Jul-23	23:04	52.4				Measured Noise Level<Limit Level	Fine	0.3
27-Jul-23	23:12	51.0				Measured Noise Level<Limit Level	Fine	0.0
01-Aug-23	23:06	53.7				Measured Noise Level<Limit Level	Fine	0.8
10-Aug-23	23:03	52.2				Measured Noise Level<Limit Level	Fine	0.3
15-Aug-23	23:04	51.8				Measured Noise Level<Limit Level	Fine	0.4
24-Aug-23	23:01	51.9				Measured Noise Level<Limit Level	Fine	0.4
29-Aug-23	23:02	52.8				Measured Noise Level<Limit Level	Fine	0.4

NMS 3 Hilton Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:52	63.0	70.9	60.2 - 78.9	55	Measured Noise Level<Baseline	Fine	0.6
09-May-23	23:26	62.9				Measured Noise Level<Baseline	Fine	0.4
19-May-23	00:38	63.1				Measured Noise Level<Baseline	Fine	0.6
23-May-23	23:23	61.0				Measured Noise Level<Baseline	Fine	0.2
02-Jun-23	00:32	63.0				Measured Noise Level<Baseline	Fine	0.4
06-Jun-23	23:22	60.3				Measured Noise Level<Baseline	Fine	0.3
16-Jun-23	00:13	62.9				Measured Noise Level<Baseline	Fine	0.2
20-Jun-23	23:33	59.0				Measured Noise Level<Baseline	Fine	0.6
30-Jun-23	00:10	62.9				Measured Noise Level<Baseline	Overcast	0.2
04-Jul-23	23:25	63.2				Measured Noise Level<Baseline	Fine	0.2
14-Jul-23	03:40	63.2				Measured Noise Level<Baseline	Fine	0.2
18-Jul-23	03:19	62.8				Measured Noise Level<Baseline	Fine	0.2
28-Jul-23	00:52	63.6				Measured Noise Level<Baseline	Fine	0.4
01-Aug-23	23:36	62.9				Measured Noise Level<Baseline	Fine	0.2
11-Aug-23	00:42	63.0				Measured Noise Level<Baseline	Fine	0.4
15-Aug-23	23:26	62.9				Measured Noise Level<Baseline	Fine	0.3
25-Aug-23	00:58	63.9				Measured Noise Level<Baseline	Fine	0.3
29-Aug-23	23:30	62.4				Measured Noise Level<Baseline	Fine	0.4

NMS 4 Tin Liu

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:24	59.6	62.6	53.1 - 68.1	55	Measured Noise Level<Baseline	Fine	0.7
09-May-23	23:34	60.6				Measured Noise Level<Baseline	Fine	1.2
18-May-23	23:23	57.0				Measured Noise Level<Baseline	Fine	0.9
23-May-23	23:32	56.8				Measured Noise Level<Baseline	Fine	0.6
01-Jun-23	23:23	58.6				Measured Noise Level<Baseline	Fine	0.7
06-Jun-23	23:28	60.5				Measured Noise Level<Baseline	Fine	0.7
15-Jun-23	23:21	56.3				Measured Noise Level<Baseline	Fine	1.2
20-Jun-23	23:36	57.0				Measured Noise Level<Baseline	Fine	0.7
29-Jun-23	23:39	61.0				Measured Noise Level<Baseline	Overcast	0.2
04-Jul-23	23:38	60.0				Measured Noise Level<Baseline	Fine	0.4
13-Jul-23	23:31	60.8				Measured Noise Level<Baseline	Fine	0.2
19-Jul-23	23:33	55.5				Measured Noise Level<Baseline	Fine	0.6
27-Jul-23	23:41	61.1				Measured Noise Level<Baseline	Fine	0.3
01-Aug-23	23:43	58.1				Measured Noise Level<Baseline	Fine	0.6
10-Aug-23	23:29	61.1				Measured Noise Level<Baseline	Fine	0.4
15-Aug-23	23:38	59.8				Measured Noise Level<Baseline	Fine	0.6
24-Aug-23	23:25	61.1				Measured Noise Level<Baseline	Fine	0.3
29-Aug-23	23:41	58.5				Measured Noise Level<Baseline	Fine	0.3

NMS 5A Wai Wah Centre (Site Boundary)

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	00:47	66.7	67.9	62.0 - 75.2	55	Measured Noise Level<Baseline	Fine	0.5
09-May-23	23:46	67.1				Measured Noise Level<Baseline	Fine	0.5
19-May-23	00:14	65.9				Measured Noise Level<Baseline	Fine	0.7
23-May-23	23:43	67.8				Measured Noise Level<Baseline	Fine	0.3
02-Jun-23	00:08	65.9				Measured Noise Level<Baseline	Fine	0.5
06-Jun-23	23:43	66.5				Measured Noise Level<Baseline	Fine	0.5
16-Jun-23	01:03	66.1				Measured Noise Level<Baseline	Fine	0.2
20-Jun-23	23:55	66.6				Measured Noise Level<Baseline	Fine	0.5
30-Jun-23	00:34	66.6				Measured Noise Level<Baseline	Overcast	0.4
04-Jul-23	23:46	66.5				Measured Noise Level<Baseline	Fine	0
14-Jul-23	02:52	65.8				Measured Noise Level<Baseline	Fine	0.5
18-Jul-23	23:44	66.5				Measured Noise Level<Baseline	Fine	0
28-Jul-23	00:27	65.3				Measured Noise Level<Baseline	Fine	0.5
01-Aug-23	23:59	66.3				Measured Noise Level<Baseline	Fine	0.4
11-Aug-23	00:20	66.0				Measured Noise Level<Baseline	Fine	0
15-Aug-23	23:49	65.9				Measured Noise Level<Baseline	Fine	0.3
25-Aug-23	00:32	65.1				Measured Noise Level<Baseline	Fine	0.2
29-Aug-23	23:53	65.8				Measured Noise Level<Baseline	Fine	0.2

NMS 6A Wai Wah Centre (Site Boundary)

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	01:08	69.6	71.5	65.0 - 85.9	55	Measured Noise Level<Baseline	Fine	0.5
10-May-23	00:04	70.1				Measured Noise Level<Baseline	Fine	0.5
18-May-23	23:53	70.0				Measured Noise Level<Baseline	Fine	0.4
24-May-23	00:02	68.9				Measured Noise Level<Baseline	Fine	0.3
01-Jun-23	23:46	70.1				Measured Noise Level<Baseline	Fine	0.6
07-Jun-23	00:01	69.8				Measured Noise Level<Baseline	Fine	0.5
16-Jun-23	01:22	70.0				Measured Noise Level<Baseline	Fine	0.4
21-Jun-23	00:14	69.5				Measured Noise Level<Baseline	Fine	0.6
30-Jun-23	00:57	69.3				Measured Noise Level<Baseline	Overcast	0.6
05-Jul-23	00:05	69.3				Measured Noise Level<Baseline	Fine	0.0
14-Jul-23	01:39	69.3				Measured Noise Level<Baseline	Fine	0.0
19-Jul-23	00:06	68.8				Measured Noise Level<Baseline	Fine	0.3
28-Jul-23	00:06	70.1				Measured Noise Level<Baseline	Fine	0.5
02-Aug-23	00:20	70.1				Measured Noise Level<Baseline	Fine	0.2
10-Aug-23	23:58	69.8				Measured Noise Level<Baseline	Fine	0.2
16-Aug-23	00:08	69.6				Measured Noise Level<Baseline	Fine	0.3
25-Aug-23	00:08	69.8				Measured Noise Level<Baseline	Fine	0.5
29-Aug-23	00:20	69.5				Measured Noise Level<Baseline	Fine	0.2

If measured noise level (Leq) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 7 Tin Liu

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:45	56.7	59.0	51.4 - 65.5	55	Measured Noise Level<Baseline	Fine	1.2
09-May-23	23:58	56.4				Measured Noise Level<Baseline	Fine	0.6
18-May-23	23:44	55.8				Measured Noise Level<Baseline	Fine	1.4
23-May-23	23:54	55.5				Measured Noise Level<Baseline	Fine	0.5
01-Jun-23	23:43	56.5				Measured Noise Level<Baseline	Fine	1.3
06-Jun-23	23:51	56.5				Measured Noise Level<Baseline	Fine	0.6
15-Jun-23	23:41	59.1				42.7*	Fine	0.5
20-Jun-23	23:58	55.7				Measured Noise Level<Baseline	Fine	0.6
29-Jun-23	23:58	59.7				51.4*	Overcast	0.2
04-Jul-23	23:59	56.2				Measured Noise Level<Baseline	Fine	0.5
14-Jul-23	00:19	53.5				Measured Noise Level<Limit Level	Fine	0
19-Jul-23	23:56	55.5				Measured Noise Level<Baseline	Fine	0.5
28-Jul-23	00:07	58.1				Measured Noise Level<Baseline	Fine	0.3
02-Aug-23	00:04	57.1				Measured Noise Level<Baseline	Fine	0.5
10-Aug-23	23:50	59.9				52.6*	Fine	0.3
16-Aug-23	00:02	57.2				Measured Noise Level<Baseline	Fine	0.4
24-Aug-23	23:45	59.9				52.6*	Fine	0.4
30-Aug-23	00:02	54.7				Measured Noise Level<Limit Level	Fine	0.4

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 8 Shatin Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:05	62.4	64.4	55.6 - 72.8	55	Measured Noise Level<Baseline	Fine	0.3
10-May-23	00:30	62.0				Measured Noise Level<Baseline	Fine	0.4
18-May-23	23:12	62.1				Measured Noise Level<Baseline	Fine	0.5
24-May-23	00:28	61.0				Measured Noise Level<Baseline	Fine	0.2
01-Jun-23	23:06	62.1				Measured Noise Level<Baseline	Fine	0.7
07-Jun-23	00:28	62.0				Measured Noise Level<Baseline	Fine	0.3
15-Jun-23	23:21	61.9				Measured Noise Level<Baseline	Fine	0.2
21-Jun-23	00:38	61.8				Measured Noise Level<Baseline	Fine	0.4
29-Jun-23	23:00	62.1				Measured Noise Level<Baseline	Overcast	0.4
05-Jul-23	00:30	61.9				Measured Noise Level<Baseline	Fine	0.2
14-Jul-23	02:04	62.2				Measured Noise Level<Baseline	Fine	0.2
19-Jul-23	00:32	62.2				Measured Noise Level<Baseline	Fine	0.2
27-Jul-23	23:24	62.0				Measured Noise Level<Baseline	Fine	0.4
02-Aug-23	00:46	62.3				Measured Noise Level<Baseline	Fine	0.3
10-Aug-23	23:18	61.9				Measured Noise Level<Baseline	Fine	0.4
16-Aug-23	00:35	62.2				Measured Noise Level<Baseline	Fine	0.2
24-Aug-23	23:25	62.4				Measured Noise Level<Baseline	Fine	0.2
29-Aug-23	00:44	61.8				Measured Noise Level<Baseline	Fine	0.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 9 Lek Yuen Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	01:36	55.9	53.5	39.5 - 63.1	55	52.2*	Fine	0.6
10-May-23	01:15	56.0				52.4*	Fine	0.3
19-May-23	01:29	56.2				52.9*	Fine	0.3
24-May-23	01:14	55.4				50.9*	Fine	0
02-Jun-23	01:29	56.0				52.4*	Fine	0.4
07-Jun-23	01:14	55.4				50.9*	Fine	0.3
16-Jun-23	01:48	55.9				52.2*	Fine	0.4
21-Jun-23	01:21	56.5				53.5*	Fine	0.2
30-Jun-23	01:22	56.0				52.4*	Overcast	0.4
05-Jul-23	01:16	56.0				52.4*	Fine	0
14-Jul-23	01:12	55.8				51.9*	Fine	0.5
19-Jul-23	01:16	56.1				52.6*	Fine	0
28-Jul-23	01:44	56.0				52.4*	Fine	0.4
02-Aug-23	01:32	55.3				50.6*	Fine	0.2
11-Aug-23	01:35	55.8				51.9*	Fine	0.2
16-Aug-23	01:21	55.4				50.9*	Fine	0
25-Aug-23	01:54	56.3				53.1*	Fine	0.2
30-Aug-23	01:29	56.0				52.4*	Fine	0.2

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 11 Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	00:49	55.7	53.2	46.1 - 62.8	55	52.1*	Fine	0.6
10-May-23	01:03	51.7				Measured Noise Level<Limit Level	Fine	0.6
19-May-23	00:46	53.7				Measured Noise Level<Limit Level	Fine	0.6
24-May-23	00:53	53.3				Measured Noise Level<Limit Level	Fine	0.3
02-Jun-23	00:45	54.3				Measured Noise Level<Limit Level	Fine	0.8
07-Jun-23	00:57	52.5				Measured Noise Level<Limit Level	Fine	0.5
16-Jun-23	00:42	53.9				Measured Noise Level<Limit Level	Fine	0.7
21-Jun-23	01:02	53.5				Measured Noise Level<Limit Level	Fine	0.7
30-Jun-23	00:58	54.1				Measured Noise Level<Limit Level	Overcast	0.2
05-Jul-23	00:48	52.7				Measured Noise Level<Limit Level	Fine	0.6
14-Jul-23	00:19	53.5				Measured Noise Level<Limit Level	Fine	0.6
19-Jul-23	01:01	54.0				Measured Noise Level<Limit Level	Fine	0.6
28-Jul-23	01:26	53.0				Measured Noise Level<Limit Level	Fine	0.3
02-Aug-23	01:17	53.5				Measured Noise Level<Limit Level	Fine	0.4
11-Aug-23	00:56	54.5				Measured Noise Level<Limit Level	Fine	0.4
16-Aug-23	01:02	53.6				Measured Noise Level<Limit Level	Fine	0.4
25-Aug-23	00:49	54.2				Measured Noise Level<Limit Level	Fine	0.4
30-Aug-23	01:06	52.3				Measured Noise Level<Limit Level	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 13 Lek Yuen Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	01:59	53.0	57.3	45.4 - 72.5	55	Measured Noise Level<Limit Level	Fine	0.2
10-May-23	01:41	54.4				Measured Noise Level<Limit Level	Fine	0.3
19-May-23	01:54	52.9				Measured Noise Level<Limit Level	Fine	0.5
24-May-23	01:38	55.0				Measured Noise Level<Baseline	Fine	0.2
02-Jun-23	01:52	53.0				Measured Noise Level<Limit Level	Fine	0.4
07-Jun-23	01:35	53.8				Measured Noise Level<Limit Level	Fine	0.4
16-Jun-23	02:08	52.8				Measured Noise Level<Limit Level	Fine	0.2
21-Jun-23	01:50	53.5				Measured Noise Level<Limit Level	Fine	0.5
30-Jun-23	01:44	52.6				Measured Noise Level<Limit Level	Overcast	0.3
05-Jul-23	01:40	53.0				Measured Noise Level<Limit Level	Fine	0.0
14-Jul-23	00:49	52.8				Measured Noise Level<Limit Level	Fine	0.2
19-Jul-23	01:39	54.3				Measured Noise Level<Limit Level	Fine	0.2
28-Jul-23	02:08	53.1				Measured Noise Level<Limit Level	Fine	0.4
02-Aug-23	01:56	52.5				Measured Noise Level<Limit Level	Fine	0.3
11-Aug-23	02:01	53.2				Measured Noise Level<Limit Level	Fine	0.2
16-Aug-23	01:46	53.3				Measured Noise Level<Limit Level	Fine	0.3
25-Aug-23	02:20	53.2				Measured Noise Level<Limit Level	Fine	0.3
30-Aug-23	01:53	53.7				Measured Noise Level<Limit Level	Fine	0.3

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 14 Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	01:20	53.7	54.1	46.1 - 62.8	55	Measured Noise Level<Limit Level	Fine	0.8
10-May-23	01:29	54.2				Measured Noise Level<Limit Level	Fine	0.6
19-May-23	01:20	54.4				Measured Noise Level<Limit Level	Fine	1.4
24-May-23	01:13	54.5				Measured Noise Level<Limit Level	Fine	0.5
01-Jun-23	01:05	54.0				Measured Noise Level<Limit Level	Fine	0.8
07-Jun-23	01:18	54.4				Measured Noise Level<Limit Level	Fine	0.6
15-Jun-23	01:01	53.9				Measured Noise Level<Limit Level	Fine	0.8
20-Jun-23	01:24	56.3				52.3*	Fine	0.6
29-Jun-23	01:17	57.0				53.9*	Overcast	0.0
05-Jul-23	01:10	55.5				49.9*	Fine	0.6
14-Jul-23	00:38	57.0				53.9*	Fine	0.2
19-Jul-23	01:21	56.0				51.5*	Fine	0.5
28-Jul-23	01:53	56.8				53.5*	Fine	0.2
01-Aug-23	01:40	56.1				51.8*	Fine	0.6
11-Aug-23	01:17	57.1				54.1*	Fine	0.4
15-Aug-23	01:28	54.4				Measured Noise Level<Limit Level	Fine	0.5
24-Aug-23	01:09	57.2				54.3*	Fine	0.5
29-Aug-23	01:27	52.7				Measured Noise Level<Limit Level	Fine	0.4

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 15 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	01:39	54.1	58.8	48.4 - 69.7	55	Measured Noise Level<Limit Level	Fine	0.8
10-May-23	01:52	56.4				Measured Noise Level<Baseline	Fine	0.5
19-May-23	01:41	54.8				Measured Noise Level<Limit Level	Fine	0.6
24-May-23	01:34	55.7				Measured Noise Level<Baseline	Fine	0.6
02-Jun-23	01:26	54.0				Measured Noise Level<Limit Level	Fine	0.9
07-Jun-23	01:39	55.5				Measured Noise Level<Baseline	Fine	0.6
16-Jun-23	01:22	53.0				Measured Noise Level<Limit Level	Fine	1.1
21-Jun-23	01:46	57.3				Measured Noise Level<Baseline	Fine	0.3
30-Jun-23	01:40	59.0				45.5*	Overcast	0.4
05-Jul-23	01:34	55.5				Measured Noise Level<Baseline	Fine	0.5
14-Jul-23	01:00	58.0				Measured Noise Level<Baseline	Fine	0.2
19-Jul-23	01:43	56.5				Measured Noise Level<Baseline	Fine	0.6
28-Jul-23	02:15	58.0				Measured Noise Level<Baseline	Fine	0.2
02-Aug-23	01:59	57.6				Measured Noise Level<Baseline	Fine	0.6
11-Aug-23	01:39	59.0				45.5*	Fine	0.3
16-Aug-23	01:50	56.1				Measured Noise Level<Baseline	Fine	0.6
25-Aug-23	01:33	59.1				47.3*	Fine	0.3
30-Aug-23	01:47	56.4				Measured Noise Level<Baseline	Fine	0.6

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 16 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	02:00	53.4	60.1	51.4 - 69.5	55	Measured Noise Level<Limit Level	Fine	1.4
10-May-23	02:11	54.6				Measured Noise Level<Limit Level	Fine	0.5
19-May-23	02:00	53.3				Measured Noise Level<Limit Level	Fine	1.4
24-May-23	01:58	56.2				Measured Noise Level<Baseline	Fine	0.6
02-Jun-23	01:46	53.4				Measured Noise Level<Limit Level	Fine	0.7
07-Jun-23	02:03	57.2				Measured Noise Level<Baseline	Fine	0.6
16-Jun-23	01:45	52.8				Measured Noise Level<Limit Level	Fine	0.2
21-Jun-23	02:08	57.6				Measured Noise Level<Baseline	Fine	0.3
30-Jun-23	01:58	58.1				Measured Noise Level<Baseline	Overcast	0.4
05-Jul-23	02:38	56.4				Measured Noise Level<Baseline	Fine	0.5
14-Jul-23	01:19	58.0				Measured Noise Level<Baseline	Fine	0.3
19-Jul-23	02:03	54.9				Measured Noise Level<Limit Level	Fine	0.5
28-Jul-23	02:42	58.2				Measured Noise Level<Baseline	Fine	0.3
02-Aug-23	02:19	56.9				Measured Noise Level<Baseline	Fine	0.5
11-Aug-23	01:58	58.0				Measured Noise Level<Baseline	Fine	0.3
16-Aug-23	02:02	54.4				Measured Noise Level<Limit Level	Fine	0.4
25-Aug-23	01:53	58.2				Measured Noise Level<Baseline	Fine	0.3
30-Aug-23	02:09	50.8				Measured Noise Level<Limit Level	Fine	0.4

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 18 Ha Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	02:22	52.0	63.2	56.0 - 72.1	55	Measured Noise Level<Limit Level	Fine	0.7
10-May-23	02:34	53.6				Measured Noise Level<Limit Level	Fine	0.6
19-May-23	02:19	52.4				Measured Noise Level<Limit Level	Fine	1.2
24-May-23	02:18	54.5				Measured Noise Level<Limit Level	Fine	0.7
02-Jun-23	02:08	52.1				Measured Noise Level<Limit Level	Fine	0.6
07-Jun-23	02:23	52.1				Measured Noise Level<Limit Level	Fine	0.6
16-Jun-23	02:04	52.7				Measured Noise Level<Limit Level	Fine	1.1
21-Jun-23	02:28	53.8				Measured Noise Level<Limit Level	Fine	0.6
30-Jun-23	02:16	54.5				Measured Noise Level<Limit Level	Overcast	0.0
05-Jul-23	02:58	53.3				Measured Noise Level<Limit Level	Fine	0.5
14-Jul-23	01:42	55.1				Measured Noise Level<Baseline	Fine	0.6
19-Jul-23	02:24	54.2				Measured Noise Level<Limit Level	Fine	0.6
28-Jul-23	03:06	54.0				Measured Noise Level<Limit Level	Fine	0.2
02-Aug-23	02:40	53.8				Measured Noise Level<Limit Level	Fine	0.3
11-Aug-23	02:18	54.9				Measured Noise Level<Limit Level	Fine	0.3
16-Aug-23	02:23	53.2				Measured Noise Level<Limit Level	Fine	0.3
25-Aug-23	02:12	55.0				Measured Noise Level<Baseline	Fine	0.0
30-Aug-23	02:31	51.9				Measured Noise Level<Limit Level	Fine	0.3

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 19 Wo Che Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	02:23	54.8	61.7	53.8 - 72.8	55	Measured Noise Level<Limit Level	Fine	0.2
10-May-23	02:10	61.6				Measured Noise Level<Baseline	Fine	0.4
19-May-23	02:22	54.6				Measured Noise Level<Limit Level	Fine	0.2
24-May-23	02:03	60.3				Measured Noise Level<Baseline	Fine	0.4
02-Jun-23	02:16	53.9				Measured Noise Level<Limit Level	Fine	0.4
07-Jun-23	01:53	54.8				Measured Noise Level<Limit Level	Fine	0.0
16-Jun-23	02:35	53.8				Measured Noise Level<Limit Level	Fine	0.3
21-Jun-23	02:18	54.6				Measured Noise Level<Limit Level	Fine	0.3
30-Jun-23	02:10	54.4				Measured Noise Level<Limit Level	Overcast	0.3
05-Jul-23	02:10	55.2				Measured Noise Level<Baseline	Fine	0.0
14-Jul-23	00:06	53.9				Measured Noise Level<Limit Level	Fine	0.4
19-Jul-23	02:11	57.9				Measured Noise Level<Baseline	Fine	0.2
28-Jul-23	02:35	54.1				Measured Noise Level<Limit Level	Fine	0.4
02-Aug-23	02:20	54.6				Measured Noise Level<Limit Level	Fine	0.3
11-Aug-23	02:28	53.9				Measured Noise Level<Limit Level	Fine	0.0
16-Aug-23	02:10	55.2				Measured Noise Level<Baseline	Fine	0.2
25-Aug-23	02:41	53.9				Measured Noise Level<Limit Level	Fine	0.2
30-Aug-23	02:18	54.4				Measured Noise Level<Limit Level	Fine	0.3

NMS 20 Wo Che Estate

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	02:44	50.2	57.7	48.6 - 71.7	55	Measured Noise Level<Limit Level	Fine	0.5
10-May-23	02:28	53.9				Measured Noise Level<Limit Level	Fine	0.3
19-May-23	02:45	49.4				Measured Noise Level<Limit Level	Fine	0.2
24-May-23	02:21	53.8				Measured Noise Level<Limit Level	Fine	0.2
02-Jun-23	02:35	49.5				Measured Noise Level<Limit Level	Fine	0.3
07-Jun-23	02:14	49.4				Measured Noise Level<Limit Level	Fine	0.0
16-Jun-23	02:54	49.9				Measured Noise Level<Limit Level	Fine	0.0
21-Jun-23	02:40	50.9				Measured Noise Level<Limit Level	Fine	0.4
30-Jun-23	02:28	50.2				Measured Noise Level<Limit Level	Overcast	0.4
05-Jul-23	02:28	51.1				Measured Noise Level<Limit Level	Fine	0.0
14-Jul-23	00:25	50.8				Measured Noise Level<Limit Level	Fine	0.4
19-Jul-23	02:30	53.2				Measured Noise Level<Limit Level	Fine	0.2
28-Jul-23	02:54	50.1				Measured Noise Level<Limit Level	Fine	0.2
02-Aug-23	02:38	49.9				Measured Noise Level<Limit Level	Fine	0.2
11-Aug-23	02:46	50.1				Measured Noise Level<Limit Level	Fine	0.0
16-Aug-23	02:30	51.0				Measured Noise Level<Limit Level	Fine	0.2
25-Aug-23	02:59	50.1				Measured Noise Level<Limit Level	Fine	0.3
30-Aug-23	02:34	50.0				Measured Noise Level<Limit Level	Fine	0.3

NMS 23 Pai Tau

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	00:08	57.1	59.9	47.8 - 69.8	55	Measured Noise Level<Baseline	Fine	0.4
10-May-23	00:18	57.6				Measured Noise Level<Baseline	Fine	0.5
19-May-23	00:05	54.8				Measured Noise Level<Limit Level	Fine	0.3
24-May-23	00:13	56.6				Measured Noise Level<Baseline	Fine	0.5
02-Jun-23	00:07	56.0				Measured Noise Level<Baseline	Fine	0.3
07-Jun-23	00:12	58.8				Measured Noise Level<Baseline	Fine	0.5
16-Jun-23	00:02	58.0				Measured Noise Level<Baseline	Fine	0.6
21-Jun-23	00:18	58.4				Measured Noise Level<Baseline	Fine	0.2
30-Jun-23	00:18	60.0				43.6*	Overcast	0.5
05-Jul-23	00:22	55.6				Measured Noise Level<Baseline	Fine	0.2
14-Jul-23	02:56	60.1				46.6*	Fine	0.2
19-Jul-23	00:19	53.9				Measured Noise Level<Limit Level	Fine	0.0
28-Jul-23	00:31	59.7				Measured Noise Level<Baseline	Fine	0.2
02-Aug-23	00:31	53.3				Measured Noise Level<Limit Level	Fine	0.2
11-Aug-23	00:14	60.0				43.6*	Fine	0.5
16-Aug-23	00:22	56.4				Measured Noise Level<Baseline	Fine	0.2
25-Aug-23	00:06	60.1				46.6*	Fine	0.5
30-Aug-23	00:24	58.2				Measured Noise Level<Baseline	Fine	0.2

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

If measured noise level (Leq) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

NMS 24 Shatin Plaza

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
04-May-23	23:24	58.8	58.0	50.2 - 66.7	55	51.1*	Fine	0.2
10-May-23	00:48	57.4				Measured Noise Level<Baseline	Fine	0.4
18-May-23	23:30	58.8				51.1*	Fine	0.4
24-May-23	00:46	57.5				Measured Noise Level<Baseline	Fine	0.2
01-Jun-23	23:24	59.0				52.1*	Fine	0.2
07-Jun-23	00:47	59.0				52.1*	Fine	0.2
15-Jun-23	23:40	58.8				51.1*	Fine	0.3
21-Jun-23	00:56	58.8				51.1*	Fine	0.5
29-Jun-23	23:19	58.9				51.6*	Overcast	0.2
05-Jul-23	00:49	59.6				54.5*	Fine	0.3
14-Jul-23	02:28	59.0				52.1*	Fine	0.3
19-Jul-23	00:51	59.5				54.2*	Fine	0.2
27-Jul-23	23:43	59.0				52.1*	Fine	0.2
02-Aug-23	00:46	58.7				50.4*	Fine	0.3
10-Aug-23	23:36	58.8				51.1*	Fine	0.4
16-Aug-23	00:54	58.8				51.1*	Fine	0.3
24-Aug-23	23:44	59.6				54.5*	Fine	0.2
30-Aug-23	01:03	58.6				49.7*	Fine	0.2

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

NMS 25A Sheung Wo Che

Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	00:27	56.3	59.7	50.3 - 68.4	55	Measured Noise Level<Baseline	Fine	0.8
10-May-23	00:40	58.2				Measured Noise Level<Baseline	Fine	0.7
19-May-23	00:27	55.0				Measured Noise Level<Baseline	Fine	0.8
24-May-23	00:33	55.0				Measured Noise Level<Baseline	Fine	0.4
02-Jun-23	00:26	56.9				Measured Noise Level<Baseline	Fine	0.6
07-Jun-23	00:34	56.3				Measured Noise Level<Baseline	Fine	0.6
16-Jun-23	00:21	57.6				Measured Noise Level<Baseline	Fine	1.0
21-Jun-23	00:39	57.2				Measured Noise Level<Baseline	Fine	0.6
30-Jun-23	00:37	54.3				Measured Noise Level<Limit Level	Overcast	0.4
05-Jul-23	02:08	56.7				Measured Noise Level<Baseline	Fine	0.6
14-Jul-23	02:37	54.2				Measured Noise Level<Limit Level	Fine	0.3
19-Jul-23	00:42	56.2				Measured Noise Level<Baseline	Fine	0.6
28-Jul-23	01:04	53.2				Measured Noise Level<Limit Level	Fine	0.4
02-Aug-23	00:55	56.0				Measured Noise Level<Baseline	Fine	0.3
11-Aug-23	00:34	54.1				Measured Noise Level<Limit Level	Fine	0.3
16-Aug-23	00:44	55.3				Measured Noise Level<Baseline	Fine	0.6
25-Aug-23	00:26	54.5				Measured Noise Level<Limit Level	Fine	0.3
30-Aug-23	00:45	57.3				Measured Noise Level<Baseline	Fine	0.4









NMS 26 Wo Che Estate






Date	Start Time	Average Leq (15 min) (dB(A))	Baseline (dB(A))	Baseline Range (dB(A))	Limit Level (dB(A))	Corrected Noise Level (dB(A))	Weather	Wind Speed (m/s)
05-May-23	02:48	58.7	61.2	45.7 - 70.1	55	Measured Noise Level<Baseline	Fine	0.7
10-May-23	02:58	60.1				Measured Noise Level<Baseline	Fine	0.7
19-May-23	02:50	55.8				Measured Noise Level<Baseline	Fine	0.4
24-May-23	02:48	58.5				Measured Noise Level<Baseline	Fine	0.2
02-Jun-23	02:40	58.1				Measured Noise Level<Baseline	Fine	0.5
07-Jun-23	02:49	60.6				Measured Noise Level<Baseline	Fine	0.7
16-Jun-23	02:40	57.1				Measured Noise Level<Baseline	Fine	1.1
21-Jun-23	02:54	60.8				Measured Noise Level<Baseline	Fine	0.5
30-Jun-23	02:40	60.8				Measured Noise Level<Baseline	Overcast	0.3
05-Jul-23	03:27	58.5				Measured Noise Level<Baseline	Fine	0.6
14-Jul-23	02:04	60.8				Measured Noise Level<Baseline	Fine	0.2
19-Jul-23	02:55	56.7				Measured Noise Level<Baseline	Fine	0.4
28-Jul-23	03:34	60.1				Measured Noise Level<Baseline	Fine	0.2
02-Aug-23	03:04	58.2				Measured Noise Level<Baseline	Fine	0.6
11-Aug-23	02:43	60.9				Measured Noise Level<Baseline	Fine	0.3
16-Aug-23	02:51	57.5				Measured Noise Level<Baseline	Fine	0.5
25-Aug-23	02:37	60.9				Measured Noise Level<Baseline	Fine	0.3
30-Aug-23	02:57	57.3				Measured Noise Level<Baseline	Fine	0.5

Note: *Corrected Noise Level in Leq (15min) dB(A) was/were lower than Limit level: 55 dB(A).

If measured noise level (L_{eq}) > limit level, Corrected noise level (CNL) is calculated as:

$$10 \times \log \left[\left(10^{\frac{\text{Measured noise level, Leq}}{10}} \right) - \left(10^{\frac{\text{Baseline noise level}}{10}} \right) \right]$$

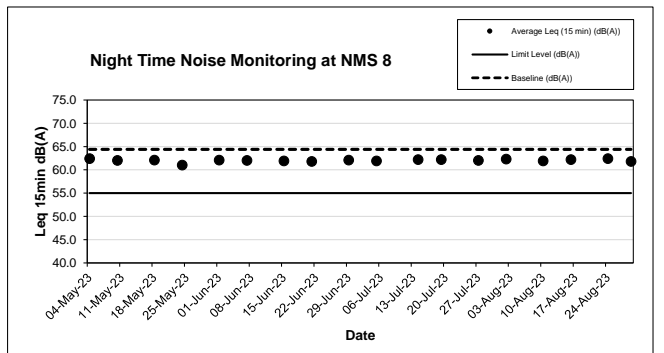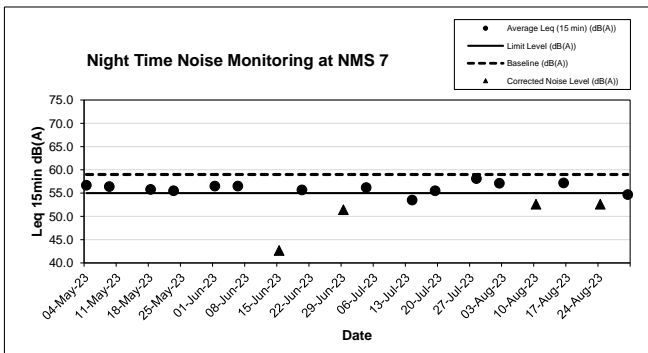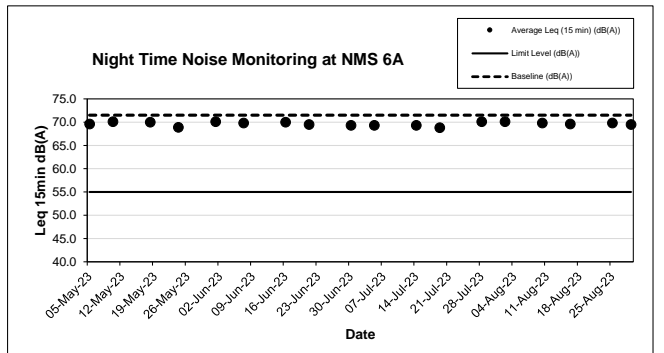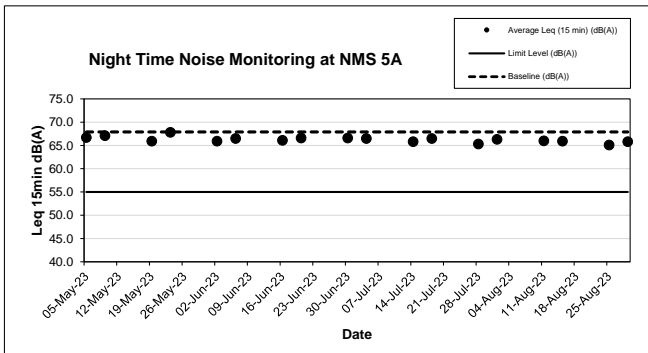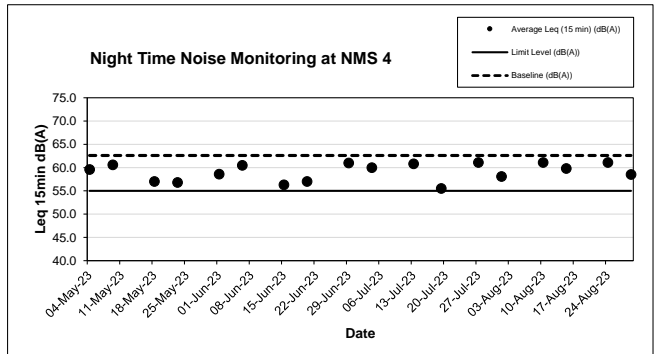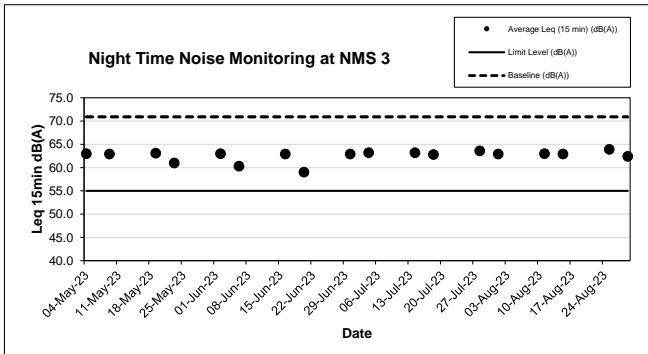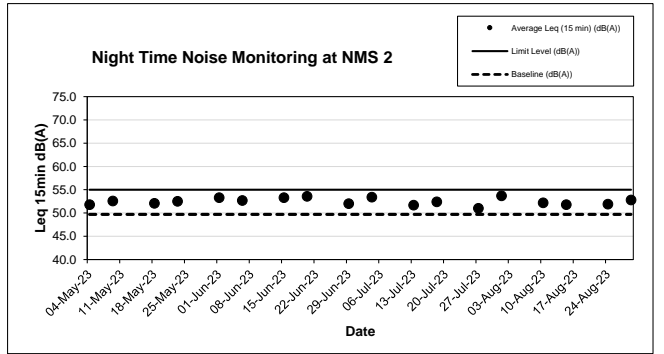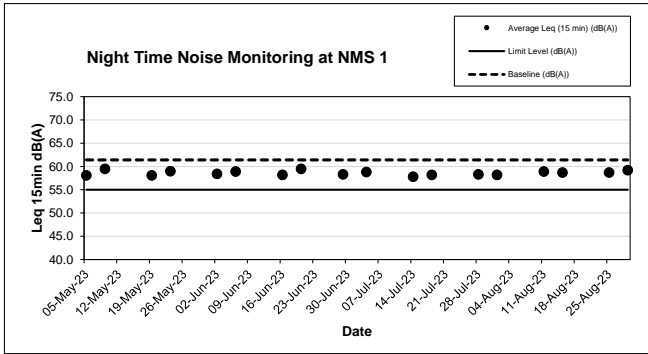

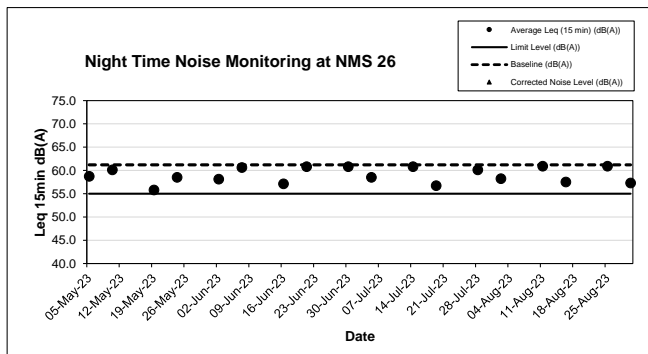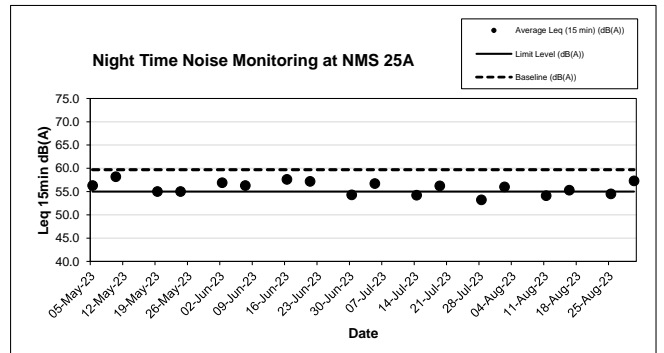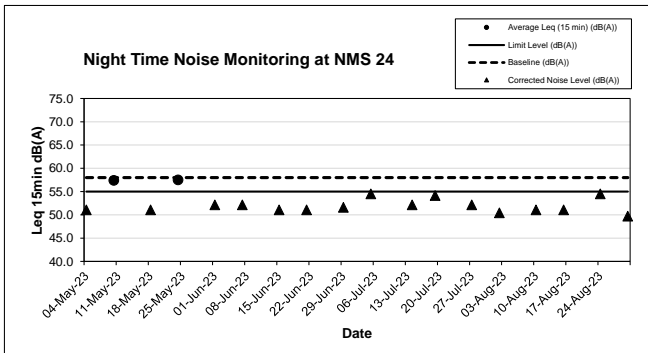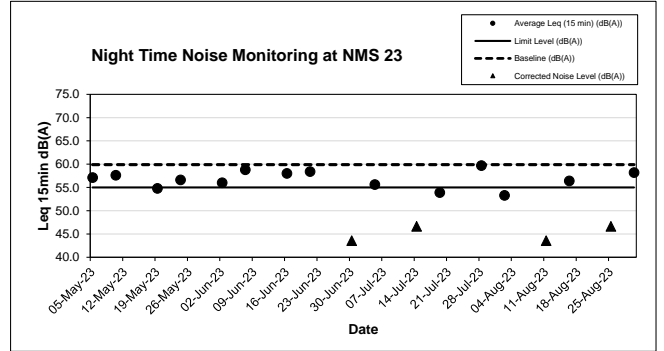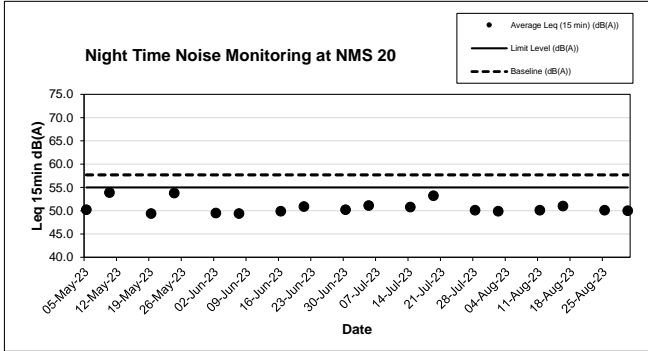

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix E

Waste Flow Table

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2018

Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2018 Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sub-Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2018 Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.013
2018 Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.004
2018 Dec	0.001	0.000	0.000	0.000	0.001	0.000	0.000	0.000	0.000	0.000	0.001
Total	0.001	0.000	0.000	0.000	0.001	0.000	0.000	0.000	0.000	0.000	0.018

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2019

Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2019 Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.021
2019 Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.049
2019 Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.048
2019 Apr	0.100	0.000	0.000	0.000	0.100	0.000	0.000	0.000	0.000	0.000	0.089
2019 May	0.150	0.000	0.000	0.000	0.150	0.000	0.000	0.000	0.000	0.000	0.175
2019 Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.082
Sub-Total	0.250	0.000	0.000	0.000	0.250	0.000	0.000	0.000	0.000	0.000	0.464
2019 Jul	0.141	0.000	0.000	0.000	0.141	0.000	0.000	0.000	0.000	0.000	0.069
2019 Aug	0.431	0.000	0.221	0.000	0.210	0.000	0.000	0.000	0.000	0.000	0.154
2019 Sep	0.712	0.000	0.223	0.000	0.489	0.297	0.000	0.000	0.000	0.000	0.046
2019 Oct	0.663	0.000	0.306	0.000	0.357	1.085	0.001	0.027	0.009	0.000	0.027
2019 Nov	1.154	0.000	0.143	0.000	1.011	0.428	0.000	0.019	0.000	0.000	0.095
2019 Dec	0.849	0.000	0.023	0.000	0.826	0.074	0.000	0.014	0.001	0.000	0.034
Total	4.200	0.000	0.916	0.000	3.284	1.884	0.001	0.060	0.010	0.000	0.889

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2020

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2020 Jan	0.584	0.000	0.027	0.000	0.557	0.040	0.001	0.030	0.001	0.000	0.039
2020 Feb	1.072	0.000	0.042	0.000	1.030	0.000	0.001	0.026	0.003	0.000	0.013
2020 Mar	0.422	0.000	0.006	0.000	0.416	0.062	0.000	0.000	0.000	0.000	0.054
2020 Apr	0.450	0.000	0.000	0.000	0.450	0.000	0.002	0.085	0.003	0.000	0.025
2020 May	1.144	0.000	0.000	0.000	1.144	0.319	0.001	0.021	0.005	0.000	0.027
2020 Jun	3.660	0.000	0.000	0.000	3.660	0.077	0.001	0.027	0.004	0.000	0.048
Sub-Total	7.332	0.000	0.075	0.000	7.257	0.498	0.006	0.189	0.016	0.000	0.206
2020 Jul	2.008	0.000	0.014	0.000	1.994	0.000	0.002	0.047	0.006	0.000	0.067
2020 Aug	2.215	0.000	0.018	0.000	2.197	0.000	0.001	0.040	0.006	0.000	0.014
2020 Sep	4.305	0.000	0.000	0.000	4.305	0.000	0.002	0.042	0.009	0.000	0.044
2020 Oct	3.073	0.000	0.002	0.000	3.071	0.000	0.001	0.019	0.005	0.000	0.029
2020 Nov	1.670	0.000	0.000	0.000	1.670	0.000	0.001	0.030	0.006	0.000	0.036
2020 Dec	3.498	0.000	0.000	0.000	3.498	0.000	24.751	0.036	0.006	0.000	0.042
Total	24.101	0.000	0.109	0.000	23.992	0.498	24.764	0.403	0.054	0.000	0.438

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2021

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2021 Jan	3.196	0.000	0.000	0.000	3.196	0.000	0.001	0.048	0.855	0.000	0.053
2021 Feb	3.877	0.000	0.000	0.000	3.877	0.032	0.000	0.010	1.642	0.000	0.013
2021 Mar	7.348	0.000	0.000	0.000	7.348	0.000	0.001	0.215	0.004	0.000	0.050
2021 Apr	3.302	0.000	0.000	0.000	3.302	0.100	0.002	0.013	0.004	0.000	0.050
2021 May	2.315	0.000	0.150	0.000	2.165	0.024	0.001	0.008	0.005	0.000	0.106
2021 Jun	1.809	0.000	0.307	0.000	1.502	0.059	0.000	0.000	0.000	0.000	0.029
Sub-Total	21.847	0.000	0.457	0.000	21.390	0.215	0.005	0.294	2.510	0.000	0.301
2021 Jul	2.693	0.000	0.000	0.000	2.674	0.262	0.003	0.011	0.007	0.000	0.119
2021 Aug	3.088	0.000	0.000	0.000	3.088	0.095	0.002	0.007	0.011	0.000	0.071
2021 Sep	1.698	0.000	0.000	0.000	1.698	0.000	0.001	0.004	0.003	0.000	0.049
2021 Oct	1.500	0.000	0.000	0.000	1.500	0.279	0.002	0.003	0.005	0.000	0.021
2021 Nov	3.258	0.000	0.000	0.000	3.258	0.015	0.002	0.009	0.007	0.000	0.070
2021 Dec	1.935	0.000	0.000	0.000	1.935	0.000	0.002	0.003	0.002	0.000	0.035
Total	36.019	0.000	0.476	0.000	35.543	0.866	0.017	0.331	2.545	0.000	0.666

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2022

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2022 Jan	1.815	0.000	0.064	0.000	1.751	0.097	20.640	0.000	0.000	0.000	0.410
2022 Feb	2.401	0.000	0.045	0.000	2.356	0.000	0.002	0.004	0.004	0.000	0.014
2022 Mar	3.039	0.000	0.000	0.000	3.039	0.037	0.000	0.000	0.000	0.000	0.026
2022 Apr	6.023	0.000	0.000	0.000	6.023	0.030	0.001	0.419	0.005	0.000	0.064
2022 May	10.291	0.000	0.000	0.000	10.291	0.159	0.001	0.011	0.003	0.000	0.042
2022 Jun	5.469	0.000	0.000	0.000	5.469	0.187	0.000	0.000	0.000	0.000	0.074
Sub-Total	29.320	0.000	0.109	0.000	29.211	0.510	20.644	0.434	0.012	0.000	0.638
2022 Jul	3.136	0.000	0.000	0.000	3.136	0.476	0.001	0.013	0.003	0.000	0.141
2022 Aug	4.111	0.000	0.000	0.000	4.111	0.431	6.871	0.373	0.010	0.000	0.088
2022 Sep	7.150	0.000	0.000	0.000	7.150	0.634	13.280	0.000	0.000	0.000	0.062
2022 Oct	8.330	0.000	0.000	0.000	8.330	1.896	0.001	0.008	0.003	0.000	0.070
2022 Nov	5.581	0.000	0.000	0.000	5.581	1.174	0.001	0.008	0.006	0.000	0.074
2022 Dec	6.787	0.000	0.000	0.000	6.787	1.134	0.001	0.003	0.001	0.000	0.080
2022 Jun	64.415	0.000	0.109	0.000	64.306	6.255	40.799	0.839	0.035	0.000	1.153

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2023

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g., general refuse
	(in '000Ton)	(in '000kg)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000Ton)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000Ton)
2023 Jan	4.592	0.000	0.000	0.000	4.592	0.322	0.000	0.002*	0.002	0.000	0.067
2023 Feb	6.448	0.000	0.000	0.000	6.448	0.500	0.001	0.281	0.003	0.000	0.055
2023 Mar	8.344	0.000	0.000	0.000	8.344	0.579	0.001	0.338	0.050	0.000	1.390
2023 Apr	5.538	0.000	0.000	0.000	5.538	1.625	0.001	0.220	0.005	0.000	0.935
2023 May	6.803	0.000	0.000	0.000	6.803	1.544	0.001	0.000	0.002	0.000	0.073
2023 Jun	8.089	0.000	0.000	0.000	8.089	0.142	0.002	0.183	0.002	0.000	0.192
Sub-Total	39.814	0.000	0.000	0.000	39.814	4.712	0.006	1.242	0.064	0.000	2.712
2023 Jul	9.764	0.000	0.000	0.000	9.764	0.041	0.001	0.200	0.004	0.000	0.144
2023 Aug	8.484	0.000	0.000	0.000	8.484	0.246	0.001	0.173	0.007	0.000	0.139
2023 Sep											
2023 Oct											
2023 Nov											
2023 Dec											
Total	58.063	0.000	0.000	0.000	58.063	4.999	0.008	1.615	0.075	0.000	2.996

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m3.
- 4) *Updated figures are present in this reporting month.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix F

Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Environmental Complaints Log

Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
COM-2019-005	2/2/2019	EPD	Noise	According to the photo taken from the complainant, the complaint was related to the project. Although the tree felling works were covered by the valid CNP (GW-RN0783-18), Contractor was reminded to strictly follow and fully comply with the CNP conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. Contractor was recommended to increase the frequency of using the electrical chain saw instead of the diesel chain saw for reducing the noise impact. Environmental Team conducted additional ad-hoc noise monitoring on 19:00 14th February 2019 to 07:00 15 th February 2019 for evaluate the effectiveness on the proposed mitigation measures. No project-related noise exceedance case on 14-15 Feb 2019 Contractor's night tree-felling and removal works. The proposed mitigation measures were effective for noise impact.	Project-related	Closed
COM-2019-006	22/2/2019	Project Hotline of NE/2017/05	Noise	According to the location of complainant from Kwai Wo House, the complaint was related to the project. Although the tree felling works were covered by the valid CNP (GW-RN0783-18), Contractor was reminded to strictly follow and fully comply with the CNP conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. An extended barrier at the top acts as a cantilever shape was recommended to modify the existing semi-enclosure installed in the cherry picker Also, three sides with top as a semi-enclosure to be used and those tree felling activities should be inside the semi-enclosure in the ground slope. The main contractor had been recommended to review their works program and methods of tree felling as to minimize the night time tree felling activities.	Project-related	Closed
COM-2019-0010	28/3/2019	Project Hotline of NE/2017/05	Noise.	The complaint case should be related to the MTR night time maintenance works. Main Contractor used portable phones and head-set only for communication, and none of loudspeakers were allowed to be used. Main Contractor handled of tree debris into the lorry skip in care when loading. Besides, a layer of soft material (soil/tree debris) was observed leaving inside the skip of the grab lorry to reduce the loading noise. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0132-19) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during	Project-non related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				restricted hour.		
COM-2019-0033	26/7/2019	Police visit on-site	Noise	The complaint is related to the project. The Main Contractor comply with CNP No.: GW-RN0443-19 allowable construction site and within the site boundary to carry out night work on tree felling and the clearance of felled tree debris during the restricted hour. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0443-19) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. Contractor was recommended to increase the frequency of using the electrical chain saw instead of the diesel chain saw for reducing the noise impact. Contractor was reminded to reschedule of tree felling arrangement that most of the fell branches and trunks were temporary laid on slope and arranged to cut smaller on Day Time to minimize the noise nuisance to the nearby NSRs.	Project-non related	Closed
COM-2019-0045	30/8/2019	1823	Noise	The complaint is related to the project. Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0443-19) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during restricted hour. Contractor should strictly follow the use of acoustic enclosure as in condition 3.d.5. of the CNP during the operation of breaker, hand-held, mass ≤ 10 kg (CNP023) shall only be operated inside the acoustic enclosure composed of four side-panels and one top-panel, so that no part of such equipment is visible from any nearby noise sensitive receiver. The panels shall be made of minimum 10mm thick plywood or 1mm thick steel outer skin and minimum 50mm thick sound absorbing lining, or equivalent construction. Contractor was reminded to use portable phones and head-set only for communication, and none of loudspeakers is allowed for night work activities.	Project-related	Closed
COM-2019-0056	9/10/2019	Project Hotline of NE/2017/05 and EPD	Noise	The complaint of the construction noise especially the breaker noise is project related. Due to the concern of road safety, the Contractor conducted the emergency road repair works under an Emergency Excavation Permit (EXP) of Plan ID: EO13123 issued by Highways Department (HyD). The main contractor's PR / hotline staff was reminded to enhance communication with sufficient information provided for replying any enquiry / complaint in the future. The main contractor was also reminded that noise mitigation measures should be provided as far as practicable subject to the emergency situation. For construction works	Project-related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				covered by the CNP issued by EPD, the main contractor should fully complied with the conditions as stipulated and provided all noise mitigation measures as required under the conditions of the CNP. For works subject to the emergency situation, noise mitigation measures such as noise barrier, enclosure etc. should be provided as far as practicable to minimise the noise nuisance to the NSRs.		
COM-2019-0057	9/10/2019	EPD	Noise	The complaint of the generator noise nuisance is related to the project. The concerned portable generator is supplying electric power for the Variable Message Sign (VMS) showing the speed limit in 50 km/hr. It is switched on and off manually by manpower, and would only be operated between daytime 07:00-19:00. No construction noise permit (CNP) should be required as the portable generator is not operating in restricted hours. The main contractor was reminded to strictly follow the use of their proposed semi-enclosure as the mitigation measures for the portable generator and the generator operates in daytime 07:00-19:00 only.	Project-related	Closed
COM-2019-0066	6/11/2019	EPD	Noise	The complaint of the emergency road repair work is related to the project. The works on on 5 th November 2019 between 22:00 and 06:00 the next day at southbound slow lane of Tai Po Road outside Wai Wah Centre, including breaking operation. The main contractor should inform the EPD in advance of any emergency opening works of the Project in future to facilitate the effective handling of noise complaint that may arise.	Project-related	Closed
COM-2020-0083	29/02/2020	Project email of NE/2017/05	Noise and Dust	The complaint of the dust and noise nuisance near Wai Wah Centre during both the day and night works was at zone 2. Contractor was reminded to enhance the water spray frequency on the construction site for mitigation measures on dust control. Also, Contractor should provide green tarpaulin curtain and additional acoustic Sound Proof Canvas as a secondary layer at the bottom of the mini-pile drilling machine to secure the total enclose condition to minimize the visual and noise impacts to nearby NSRs.	Project-non related	Closed
COM-2020-0089	24/03/2020	Project hotline	Noise	A resident of Wai Wah Centre complained that noise generated from construction activities at night disturbing the nearby resident. Loading/unloading, steel bar cutting, steel plate grinding and asphalt compaction were carried out in the early hours of 24 th Mar 2020. The night work activities were within the site boundary. Also, 4 sides with top cover acoustic enclosure for	Project-non related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				the portable generator was used during the night work. Furthermore, mitigation measures listed in the CNP were implemented for PME and works activities. Three sides with top cover enclosure and additional acoustic comprised with 50 mm sound absorbing lining were used for night works activities.		
COM-2020-0090	27/03/2020	Project hotline	Noise	Both complaint cases were concerning about the noise nuisance generated from the construction work activities at night time disturbing the nearby Wai Wah Centre residence. According to the Main Contractor, similar nature of major construction works carried out between 03:00 a.m. and 04:00 a.m. on 27 th & 28 th March 2020 was the asphalt compaction for the road surface remedial works at zone 2 south lane adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0002-20 that is within the allowable construction site location and within the site boundary to carry out night work on loading and unloading works. ET conduct regular night-time noise monitoring at all monitoring stations between 23:00 26 th March 2020 to 04:00 27 th March 2020, and between 23:00 2 nd April 2020 to 04:00 3 rd April respectively. No exceedance cases were found on both ET regular night-time noise monitoring measurement. ET did not remark on-site any noise related to construction works at above noise monitoring nights for which the results were lower than baseline noise level.	Project-non related	Closed
COM-2020-0091	28/03/2020					
COM-2020-0093	06/04/2020	Project hotline	Noise	The complaint case on 6 th Apr was received by project hotline. The major construction works between (10:00pm – 11:00pm) on 6 th April 2020 was TTA implementation works and asphalt removal works for the road surface remedial work at zone 2 adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0152-20 that is within the allowable construction site location and within the site boundary to carry out night work on loading and unloading works. The five noise monitoring stations close to the concerned works area are NMS3, NMS4, NMS5A, NMS6A & NMS7, and NMS5A & NMS6A locate nearest to Wai Wah Centre. The night time noise monitoring results measured at NMS3, 4 & 6A were all lower than that of measured in the baseline, two exceedance case were found at NMS 5A especially NMS 5A & NMS 6A monitoring stations where locate at the Wai Wah Centre. The corrected noise level measured at NMS 7 is lower than the night	Project-non related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				time limit 55dB (A). Therefore, there was no exceedance cases were found on ET regular night-time noise monitoring measurement.		
COM-2020-0096	20/04/2020	Project hotline	Noise	<p>A continues complaint were received on 20 Apr and 21 Apr 2020. A resident of Wai Wah Centre filed three complaints about the noise nuisance generated by the nearby construction activities during daytime. Two complaints were made through project hotline on 20th Apr 2020 at 10:57 a.m. and 21st Apr 2020 at 9:03 a.m., while the other one was through project email on 20th Apr 2020 at 12:43 p.m. The noise source(s) of the concerned nuisance during complaint period should be mini piling works, which is opposite to Wai Wah Centre.</p> <p>According to the contractor's work schedule, major day work activity was mini-piling operation since early Feb 2020 at zone 2 in central median at non-restricted hours, from Mondays to Saturdays between 0800 and 1800 not including General Holidays. The mini piling operation on 20th & 21st Apr 2020 was carried out at non restricted hours. The limited level of noise generated by the construction of the Project during the non-restricted daytime hours will be 75 dB (A) for dwelling. The mini piling operation on 20th and 21st Apr 2020 was carried out at non restricted hours with green tarpaulin curtain and sound proof canvas. The noise level of NMS 5A and NMS 6A on 22nd Apr 2020 were 73.5 dB (A) and 72.6 dB (A) respectively. No noise exceedance was occurred at NMS 5A and NMS 6A. The construction activity on 22nd Apr 2020 was similar to 20th and 21st Apr 2020. Therefore, ET's day-time monitoring result on 22nd April 2020 at NMS5A and NMS6A can act as a reference for impact noise from the similar mini-piling operation on 20th and 21st April 2020.</p>	Project-non related	Closed
COM-2020-0097	20/04/2020	Project Email				
COM-2020-0098	21/04/2020	Project hotline				
COM-2020-0099	21/04/2020	Project hotline	Noise	<p>The complaint cases on 21st Apr 2020 was received by project hotline from Police.</p> <p>According to the complainant who is the local resident at Wai Wah Centre, the noise source(s) of the concerned nuisance during night works was at zone 2 is opposite to Wai Wah Centre. The major construction works was road surface remedial work since 15th April 2020 conducted at restricted hours along zone 2 south boundary adjacent to Wai Wah Centre. The Main Contractor complied with CNP No.: GW-RN0152-20 that is within the allowable construction site location and within the site boundary to carry out night work on road surface remedial</p>	Project-non related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				works. Environmental Team (ET) conduct a regular night-time noise monitoring at all monitoring stations between 23:00 23 rd April 2020 to 04:00 24 th April 2020. The five noise monitoring stations close to the concerned works area are NMS3, NMS4, NMS5A, NMS6A & NMS7, and NMS5A & NMS6A locate nearest to Wai Wah Centre. There were no exceedance on the night time noise monitoring, especially measured at NMS 5A & NMS 6A where locate at the Wai Wah Centre, the measured result at NMS 5A & 6A were all lower than that of measured in the baseline. Therefore, no exceedance cases were found on ET regular night-time noise monitoring measurement.		
COM-2020-0100	23/04/2020	Project hotline	Noise	The complaint was received via project hotline on 23 rd April 2020 at 10:45 a.m. A resident of Wai Wah Centre complained that noise generated from operation of the two piling machines disturbing her daughter's study for DSE examination, and demanding limitation on operation hours of the machines only at two separate periods between 12 noon and 1p.m and 3 p.m. to 6 p.m. According to the Main Contractor, the major construction works at day time (08:00-18:00) on 23 rd April 2020 was mini-piling operation at Zone 2 Central Median of Tai Po Road near Wai Wah Centre. According to the photo records of day-time site condition on 23 rd April 2020 provided by Main Contractor, the green tarpaulin curtain was provided for the mini-pile drilling machines so that the bottom part of the mini-pile drilling machine was blocked from view of nearby NSR (e.g. residents at Wai Wah Centre) and an additional layer of sound proof canvas was installed at lower level to mitigate the noise from mini-pile drilling operation. The day-time noise monitoring results measured at NMS3, 4, 5A, 6A and 7 were all lower than the limit level, especially NMS 5A & NMS 6A monitoring stations where locate at the Wai Wah Centre. The monitoring results show no noise exceedance occurred at both locations. Thus, ET day-time monitoring result on 22 nd April 2020 at NMS5 & NMS6 can be act as a reference for impact noise from the similar mini-piling operation activities on 23 rd April 2020. Therefore, there was no exceedance cases were found in ET regular day-time noise monitoring measurement.	Project-non related	Closed
COM-2020-0101	28/04/2020	1823 (CASE#3-	Noise	The complainant on via ICC1823 on 28 th April 2020 complained about the noise and odor nuisance generated from the night-time asphalt laying construction	Project-non	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
		631675981 7)		works at Shatin Rural Committee Road (Zone 3) area. Although the main contractor no work at zone 3, but the major night-time construction works was road surface remedial work which was related to the complainant concerned. The major construction works was road surface remedial work since 15 th April 2020 at approved restricted hours along zone 2 south boundary adjacent to Wai Wah Centre. Also, Tai Po Road is the main strategic route, implementation of temporary traffic diversion at day time due to loading and unloading material or plant work or road surface remedial work is not feasible. The lorry had been used in TTA implementation & road opening, portable generator and electric handheld breaker had been used in asphalt removal work, dump truck with grab had been used for loading and unloading of asphalt or rubble, vibratory compactor had been used in asphalt compaction for road surface remedial works on 27 th & 28 th April 2020. The Main Contractor complied with CNP No.: GW-RN0152-20 that allowed PME used in Group C or Group F. According to the Main Contractor, advance "Notice to Affected Residents" had been issued and distributed on 26 th March 2020 in accordance with the CNP advice that prior notification should be given to nearby residents. Besides, the road re-surfacing work would be carried out at approximately 14 night-time works between 2 nd and 28 th April 2020 listed in the distributed notices. No exceedance cases were found on ET regular night-time noise monitoring measurement at all noise monitoring stations, especially measured at NMS 5A & NMS 6A where locate close to the works area (Wai Wah Centre in Zone 2), the measured result at NMS 5A & 6A were all lower than that of measured in the baseline.	related	
COM-2020-0151	10/11/2020	EPD (EPD ref.: RN25799- 20)	Water	The complainant on 10 th November 2020 complained about water discharge onto the traffic lanes of Northbound towards Sha Tin Section of Tai Po Highway. According to the Main Contractor, there is one active site access located at Zone 1 (R1) near Pai Tau, site access no. is N02. Restricted opening hours of the site access Zone 1 (R1) is between 10:00 to 16:00. The operation which might be related to the complaint was water flow from water-filled barriers before the opening of site access and no water spilling onto the traffic lanes from the access area of Zone 1 (R1). The released water was directed towards to the	Project- non related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				work areas facing Zone 1 (R1) and no water was flowed towards the high-speed road or traffic lanes. ET conducted ad-hoc site inspection on 17 th November 2020. ET had no particular findings related to the complaint and conducted trial to open the bottom of the water barrier valve for testing and checking on the water flow to the construction site at Zone 1. Contractor performed well on environmental preventive measures for soil or silt leakage protection as impervious sheet with sand bags had been provided at the site boundary of Zone 3. ET analyzed that released water was directed towards to the work areas facing Zone 1 (R1) and no water was flowed towards the high-speed road or traffic lanes.		
COM-2020-153	20/11/2020	1823 (CASE#3-6561393465)	Noise	The complainant on via ICC1823 on 20 th November 2020 complained about the noise generated from the night-time asphalt laying construction works between Sha Tin Station and nearby Wo Che Estate. Although the main contractor no work at zone 5, but the major night-time construction works was road surface remedial work which was related to the complainant concerned. According to the Main Contractor, the major construction works was road surface remedial work since 19 th November 2020 conducted at restricted hours along zone 3 to zone 4 north bound of Tai Po Road Sha Tin section. No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix F) at all noise monitoring stations. Contractor placed acoustic enclosure "SilentCUBE" with four sides and a top cover at asphalt removal works to mitigate. The Main Contractor was reminded to pay attention to CNP other condition 3.d.3, the electric hand-held breaker shall only be used for carrying out construction work between 22:00 – 23:30 hours. It is prohibited to use the electric hand-held breaker beyond the CNP condition 3.d.3 stated that the using limitation on 23:30. The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during 00:00 to 06:00 sleeping time.	Project related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
0064/18/ED/0546A	24/11/2020	EPD	Water	According to EPD Mr. Bryan Kwok, EPD carried out a site inspection on 24 November 2020, revealing that muddy effluent was discharged from an outfall at Fo Tan near Jockey Club Ti-I College while construction work of the abovementioned project site at Zone 5 opposite to Wo Che Estate was in progress. EPD team inspected the condition of waste water treatment facilities on site (slope F133) and observed that the water in the first and second sedimentation tanks was muddy; muddy water was observed at the outlet level of the Wetsep (waste water treatment plant) though there was no discharge and piling works at the time. EPD team reminded the Main Contractor that effluent does not comply with the discharge license standard should NOT be allowed to discharge. The waste water treatment system should be improved and maintained to ensure the effluent discharge standard. EPD team requested in both works area of Slope F133 and Slope F163 the Main Contractor to locate the network of drainage, connecting manhole(s) and downstream manhole, check if any presence of muddy materials and clear-out. The main contractor was reminded to strictly follow and fully comply with the water discharge license (WT00032446-2018) conditions and the mitigation measures stipulated in the EM&A Manual for effluent discharge on the wastewater treatment system.	Project related	Closed
COM-2020-154	27/11/2020	1823 (CASE#3-6561393465)	Noise	The complaint was received via ICC1823 on 27 th November 2020, the complainant expressed concern of construction noise nuisances near Wo Che Estate at around 01:14 am on 27 th November 2020. According to the Main Contractor, there were no construction works near Wo Che Estate (Zone 5) on 26 th and 27 th November 2020. The major construction works were works related to removal of central median (at night-time) under the approved road closure with CNP no.GW-RN0799-20. According to Main Contractor EO Kimberly, she sent prior notification to the EPD on 20 th November 2020 through logging in the webpage of EPD before the commencement of the construction work in relation to the CNP GW-RN0799-20 (conditions 3.d.11 and 4.d.8). The Main Contractor provided photo records showing that mitigation measures of the movable acoustic enclosure "SilentCUBE" with four sides and a top cover were implemented for night work on removal of existing central median: drill hole with percussive drill for temporary steel module spiral installation, drill hole at existing	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				central median with concrete corer and asphalt compaction with portable roller. Main Contractor was reminded to strictly follow and fully comply with the CNP No.: GW-RN0799-20 conditions. 5.11. The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during 00:00 to 06:00 sleeping time.		
COM-2020-155	26/11/2020	1823 (CASE#3-656631592 2)	Dust	<p>According to the complainant, the dust nuisance concerned at day time was at the slip road to Fo Tan Road near Lok King Street near Zone 5 works area. According to the Main Contractor, the major day time construction works at Zone 5 works area in November were mini-piling works and slope works of soil replacement. Regular movement of vehicle for transportation was also carried out on site. Thus, the complaint was considered to be related to the project. ET conducted regular day-time air quality monitoring in November 2020 and on the 3rd December 2020 at selected air monitoring stations AMS6, 8, 11A & 13 and AMS5, 4A, 7A & 12 respectively.</p> <p>The two air quality monitoring stations closed to the works area at zone 5 (where the complainant concerned of dust nuisance) were AMS12 and AM13; and AMS13 locate nearest to Zone 5. The ET regular air quality results measured at AMS13 and AM12 in November 2020 and on the 3rd December 2020 show that there was no exceedance case found in air quality monitoring measurement and the results were all below the action level. The Main Contractor was reminded to enhance the mitigation measures in dust control such as increase the water spray frequency at the construction site to suppress dust emission. The Main Contractor proposed to properly maintain the coverings on exposed slopes and keep them in good condition for minimizing dust impact. The Main Contractor proposed to frequently spraying of haul road especially at area where active movement of vehicles and pave the haul road where necessary to reduce dust impact.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
COM-2020-157	07/12/2020	STDC	Dust	According to the complainant, the dust nuisance concerned at day time was generated from the construction works area of the Tai Po Road Widening project at Zone 5. According to the Main Contractor, major day time construction works of mini-piling and soil replacement at slopes were carried out at Zone 5 works area in December 2020. There was also regular movement of vehicle for transportation within the works area. Thus, the complaint was considered to be related to the project. ET conducted regular day-time air quality monitoring on the 3rd, 9th & 15th December 2020 respectively which was close to the date of complaint, at selected air monitoring stations AMS5, AMS4A, AMS7A & AMS12. ET regular day-time air quality monitoring measurement results at air quality monitoring stations AMS12, closest to Zone 5. The ET regular air quality results measured at AM12 on 3rd, 9th & 15th December 2020 show that there was no exceedance case found in air quality monitoring measurement and the results were all below the action level. The Main Contractor was reminded to reduce the travelling speed of transportation vehicles on site and plan the schedule of delivery transport in order to reduce dust impact. The Main Contractor proposed to continue in maintaining the coverings on exposed slopes in good condition for minimizing dust impact. The Main Contractor proposed to increase water spraying at area where active movements of vehicle transportation occur.	Project Related	Closed
COM-2020-161	18/12/2020	EPD	Noise	The complaint was received via email notification by EPD on 18th December 2020, the complainant expressed concern of construction noise nuisances near Wo Che Estate during night-time on 7 th & 8 th December 2020. According to the Main Contractor, the major construction works was removal of central median works since 7 th & 8 th December 2020 conducted at restricted hours along Zone 4 central median of Tai Po Road Sha Tin section. Thus, the complaint is considered to be related to the project. According to the Main Contractor, portable generator with hand-held breaker had been used for breaking of asphalt (on existing central median edge); lorry with crane, portable generator and concrete corer had been used for remove (lifting) the existing central median and coring of central median joint; dump truck with grab had been used for loading and unloading of rubble; portable roller had been used in asphalt compaction; lorry with crane, percussive and hand-held drill and portable generator had been	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				used for installation of temporary steel module between 00:30 to 04:30 am on 7 th December 2020. The Main Contractor complied with CNP No.: GW-RN0799-20 that allowed the usage of PMEs. The noise emanated from the concrete corer for drilling hole at existing central median and portable roller for asphalt compaction might cause a noise nuisance. To further alleviate the noise nuisance, the Contractor placed acoustic enclosure "SilentCUBE" with four sides and a top cover at removal of existing central median and asphalt compaction works to mitigate as shown in the site condition photo record. No exceedance cases were found on ET regular night-time noise monitoring measurement at all noise monitoring stations, especially measured at six noise monitoring stations where locate close to the works area (Sha Tin station to nearby Fung Wo Estate in Zone 4), the measured result at NMS16, NMS18 and NMS26 were lower than that of measured in the baseline. Besides, the measured result after correction of baseline at NMS13, NMS14 and NMS15 were lower than that of the limit level. The Main Contractor was reminded to re-arrange their proposed night-time construction activities especially in quiet construction works to minimize the noise nuisance to nearby residences. The Main Contractor was reminded to re-arrange their proposed night-time construction activities to fulfill the complainant expectation that noise emitting work should be paused during night sleeping time.		
COM-2020-167	22/02/2021	1823	Dust	A complainant who did not wish to disclose his identity called 1823 hotline on 22nd February 2021 regarding the dust nuisance at slip road to Fo Tan Road. A repetitive case with reference no. 3-6566315922 was referred to the Main Contractor of the captioned Project and ET on 23rd February 2021. According to the complainant, the dust nuisance concerned at day time was at the slip road to Fo Tan Road near Zone 5 works area. According to the Main Contractor, the major day time construction works at Zone 5 works area in February 2021 was mini-piling works. Regular movement of vehicle for transportation was also carried out on site. Thus, the complaint was considered to be related to the project. The Main Contractor was reminded to reduce the travelling speed of transportation vehicles on site and plan the schedule of delivery transport in order to minimize the dust impact. The Main Contractor proposed to reduce the	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				exposed surface by providing covers or paving (e.g. with cement grout) to the newly excavated slope.		
COM-2020-168	20/02/2021	1823	Noise	The complaint was received via 1823 on 20 th February 2021 01:00am concerning about the night-time construction works near Sha Tin Police Station at 19 th 20 February 2021. According to the Main Contractor, there was night-time construction works near Sha Tin Police Station (Zone 3 & 4) on 19 th 20 February 2021. The major construction works were lane shifting works conducted on 19 th 20 February 2021 at night-time under approved road closure setup with in-force Construction Noise Permit (CNP) no.GW-RN0798-020. According to the Main Contractor, since Tai Po Road is the main strategic route, implementation of temporary traffic diversion at day time due to loading and unloading material or plant work or road surface remedial work is not feasible. The concerned night work could only be conducted during off-peak period at night time under temporary traffic diversion to avoid causing traffic congestion. According to the Main Contractor, no concurrent operation of Power Mechanical Equipment (PME) and idling were switched off during the loading and unloading of materials and rubble by manual handling of road surface remedial works. Environmental Team (ET) conduct a regular night-time noise monitoring at all monitoring stations between 23:00 25th February to 03:00 26th February 2021. The five noise monitoring stations close to the complaint receiving area of Zone 3 & 4 are NMS13, NMS14, NMS15, NMS16 & NMS26. No exceedance cases were found on ET regular night-time noise monitoring measurement at all noise monitoring stations, especially measured at five noise monitoring stations where locate close to the works area (near Sha Tin Police Station in Zone 3&4), the measured result at NMS15, NMS16 and NMS26 were lower than that of measured in the baseline. Besides, the measured result after correction of baseline at NMS13 and NMS14 were lower than that of the limit level in 55 dB(A). The Main Contractor was reminded to strictly follow and fully comply with the CNP (GW-RN0798-20) conditions and the mitigation measures stipulated in the EM&A Manual when construction activities are operating during the restricted hour.	Project Related	Closed
COM-2021-0170	03/03/2021	1823	Dust and Noise	The complaint on 3rd March 2021 at 1:25 pm complained about the noise, dust and nuisance generated and insufficient dust mitigation works during the night-time	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				construction works near King Wo House and Wo Che Estate area. A repetitive case with reference no. 3-6638500887 was referred to the Main Contractor and ET of the captioned project on 4th March 2021. According to the Main Contractor, there was night time road works at King Wo House and Wo Che Estate (Zone 4 & 5) on 3rd March 2021. Thus, the complaint considered to be related to the project. According to ET investigation, the Main Contractor complied with the CNP No.: GW-RN0798-020, with the permission of using Powered Mechanical Equipment (PMEs). No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix G). The Main Contractor was reminded to close all the doors of the acoustic enclosure, included the "SilentCUBE" for hand-held breaker and metallic enclosure. Consider the dust nuisance, no exceedance cases were found on ET regular air quality monitoring measurement (Appendix F). According to the Main Contractor, vapour was emitted from the bottom of the miller, when the milled asphalt falling from the drop point of the conveyor belt to the dump truck container, fugitive dust was generated. The Main Contractor was reminded to enhance the water spray frequency and keep the road surface wet before milling as the mitigation measures on fugitive dust control.		
COM-2021-0172	03/03/2021	1823	Noise	The second complaint was received on 3rd March 2021 at 1:40 pm complained about the noise nuisance generated during the night-time construction works near Shatin Pui Ying College area. A repetitive case with reference no. 3-6638578830 was referred to the Main Contractor and ET on 8th March 2021. According to the main contractor, there was a night-construction activity near Shatin Pui Ying College and Wo Che Estate (Zone 4 & 5). Thus, the complaint considered to be related to the project. According to ET investigation, the Main Contractor complied with the CNP No.: GW-RN0798-020, with the allowed usage of PMEs. No exceedance cases were found on ET regular night-time noise monitoring measurement (Appendix G). The Main Contractor was reminded to strictly follow and fully comply with the CNP No.: GW-RN0798-20 conditions and the mitigation measures stipulated in the EM&A Manual when construction activities were operated during the restricted hour. The contractor was also reminded to use a movable noise barrier/blanket to block the line of	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				sight from the engine or noise emission part to the nearby NSRs when using PMEs.		
COM-2021-0193	09/05/2021	1823	Noise	The complaint was first received on 6 th May 2021 at 9:27 a.m. via FEHD email. The complaint was then referred to 1823 case: 3-6727963845 on 9 th May 2021 at 2:52 p.m. A follow-up complaint was received on 11 th May 2021 at 8:20 a.m. The two complaints were referred from 1823 to CEDD on 14 th May 2021 at 6:26 p.m. The complaint cases was referred from AECOM to ET on 17 th May 2021 at 11:46 a.m. According to the Main Contractor, the major construction works at daytime (08:00-18:00) between 6 th to 11 th May 2021 near Mei Wo House were soil replacement works (involved excavation, loading and unloading of materials and pour the no fine concrete) at the works area 1 (between Wo Che Estate King Wo House and Shatin Pui Ying school) and demolition of existing central divider works (involved breaking, loading and unloading of materials) at the work area 2 (opposite to Wo Che Estate Man Wo House). The ET regular daytime noise monitoring measurement results of NMS16, NMS17, NMS18, NMS19, NMS20 & NMS26 on 6 th , 7 th , 12 th and 13 th May 2021, no exceedance case found. The noise monitoring results were lower than the noise limit of 75 dB(A) L_{eq} (30 minutes) at the facade of dwellings and 70 dB(A) L_{eq} (30 minutes) at the facades of schools (65 dB (A) during examinations). The Main Contractor installed an acoustic blanket, enclosed at the breaker to minimize the noise impacts to nearby NSRs. The Main Contractor was reminded to maintain the newly implemented noise mitigation measure during breaking works. The Main Contractor was reminded to provide additional mitigation measures to minimize the noise nuisance to the NSRs (similar to night-time construction works) during the construction works, for example moveable noise barrier or blanket to block the line of sight from the engine and noise emission parts to the nearby NSRs.	Project Related	Closed
COM-2021-0200 and COM-2021-0202	07/06/2021	1823	Noise	Ms. So, a resident of Wo Che Estate, Mei Wo House complained about the noise generated from the daytime construction work located outside Mei Wo House, the tunnel entrance (direction towards Fo Tan). Until 7 th June 2021, total six complaints were received via 1823 (case: 3-6727963845) from the same complainant. According to the Main Contractor's daytime working schedule from 12 th May to 7 th June 2021 at zone 5 were soil replacement works (involved	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				excavation, loading and unloading of materials, pour the no fine concrete and formation of haul road) and demolition of existing central divider works (involved loading and unloading of materials, minor breaking and corning operation). According to CEDD, a reply was sent to Ms. So on 27 th May 2021. The Resident Site Staff (RSS) of AECOM contacted the complainant on 7 th June 2021 night to explain the detail of upcoming construction work and associated noise mitigation measures to minimize the construction noise arising from the concerned construction work. The complainant was also informed that she could contact the RSS directly if she had any further enquiry in future. ET conducted regular daytime noise monitoring at NMS16-20 and NMS26 monitoring stations on 6 th , 7 th , 12 th , 13 th , 17 th , 18 th , 24 th , 25 th of May and 4 th , 5 th , 10 th , 11 th of June 2021. No exceedance case was found and the noise monitoring results were lower than the noise limit of 75 dB(A) $L_{eq(30\text{ minutes})}$ at the facade of dwellings and 70 dB(A) $L_{eq(30\text{ minutes})}$ at the facades of schools (65 dB (A) during examinations). ET reminded the Main Contractor to implement additional mitigation measures to minimize the noise nuisance generated from daytime construction works to the nearby Noise Sensitive Receivers (NSRs). The Main Contractor agreed to install an acoustic blanket, enclosed at the breaker to minimize the noise impact generated from the demolition of central divider works. The Main Contractor was reminded to maintain the noise mitigation measure during the breaking works. The Main Contractor was reminded to provide additional mitigation measures during the construction works to minimize the noise nuisance to the NSRs (similar to nighttime construction works), for example, a temporary moveable noise barrier to lower the noise impact and an acoustic blanket to block the line of sight from the engine and noise emission parts to the nearby NSRs. The Main Contractor was also reminded to display the project hotline number 5613-3367 on-site for public enquiry.		
EN-2021-0094	26/07/2021	EPD	Air (Odour)	A resident of Paris Park Villa complained about the poor air quality around his living area between 19 th and 26 th July 2021. He suspected that the odour nuisance may be generated from the construction site's diesel machineries. The complaint was received by the EPD's Regional Office (North) on 26 th July 2021 with reference no.: RN17367-21.	Project Non-Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>According to the Main Contractor's daytime working schedule between 19th July and 26th July 2021 involved: (1) Zone 4 and 5 North boundary, the construction activities involved the formation of temporary access, backfilling works for noise barrier stem wall, loading and unloading works. Excavations were mainly performed in areas EX1 and EX2. (2) Zone 4 and 5 South boundaries, the construction activities involved the noise barrier foundation works and the formation of temporary access. Excavations were mainly performed in areas EX3 and EX4. While rebar fixing and formwork erection were also carried out in EX3 area. For area TW1 in Zone 5 South boundary, tree works were performed. There were no work activities carried out at night-time, Sunday and under the hosting of typhoon signals.</p> <p>According to AECOM's Resident Engineer and the Main Contractor, no particular malpractice was observed during the construction activities at Zone 4 and 5 between 19th and 26th July 2021. According to the Main Contractor, only machineries with valid NRMM labels and regular maintenance are being used on-site. The Main Contractor sent the Ultra-Low Sulphur Diesel (ULSD) sample for laboratory testing since Feb 2019. There is no exceedance of the Sulphur content of more than 0.005% by weight in the past and the latest sample collected on 7th July (Cap. 311I Air Pollution Control (Fuel Restriction) Regulations).</p> <p>No particular finding on odour nuisance was found by the ET's staff when performing air monitoring in AMS 14 Ha Wo Che (close to 73A Ha Wo Che) on 21st and 22nd July 2021. ET also inspected the construction site on 29th July 2021 (between 9:00 to 10:15 a.m., weekly environmental inspection). There was no particular observation on odour nuisance or diesel smell generated from the Non-Road Mobile Machineries (NRMMs) and construction activities in the North and South boundary at Zone 4 and 5. No dark smoke was observed from the excavator, power generator, pilling and pre-drilling machines under operation. ET inspected the area around Paris Park Villa and Ha Wo Che on 29th July 2021 between 10:30 a.m. to 11:30 a.m. There was no particular finding on odour nuisance in AMS14 Ha Wo Che (close to 73A Ha Wo Che).</p> <p>ET reminded the Main Contractor to strictly implement the air pollution control</p>		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				measures and minimize the air pollution impact generated from the construction work activities. The Main Contractor also is reminded that only approved or exempted NRMMS include regulated machines and non-road vehicles with proper labels are allowed to be used in specific activities on-site. The NRMMS should be well maintained. The Main Contractor was also be reminded that odour emissions from construction sites need to be controlled. Potential emission includes particulate matter, diesel and hazardous chemicals need to be considered for their odour impact. Use of ULSD should be maintained and dark smoke emission should be prevented in accordance with the Air Pollution Control (Smoke) Regulation and ETWB TCW 19/2005. The Main Contractor was also be reminded to display the project hotline number 5613-3367 on-site for public enquiry.		
DSD Ref: MS 8/0/CE2815 /0 pt.6	01/09/2021	DSD	Water	<p>Drainage Services Department (DSD) issued a notice (Ref: MS 8/0/CE2815/0 pt.6) to the Engineer's Representative (AECOM) after their morning inspection on 1st September 2021 concerning the improperly treated water being discharged from the construction site near Fung Wo Estate of the Project to nearby public stormwater drainage system, and of the consequence of contaminating the watercourse at Shing Mun River. The letter of concern was referred to Environmental Team (ET) on 2nd September 2021 at 3:24 p.m. for investigation.</p> <p>According to the Main Contractor and AECOM, the major construction work at Zone 5 south boundary was mini-pilling works (at the end of August). Two pilling machines were operating either individually or simultaneously. There are approximate 130 nos. of pile planned to be installed, and mini-piling works are scheduled to be finished in January 2022. Originally, one WetSep (TW-WS1) and two sedimentation tanks (ST1 and ST2) were provided for handling the wastewater generated from the pilling works and site surface runoff at the zone 5 south boundary. According to the information report and photo records provided by the Main Contractor, the sedimentation tanks (ST1 and ST2) were filled with muddy water and silt on 1st September 2021.</p> <p>ET inspected the area at Zone 5 south boundary on 2nd, 9th, 16th and 29th September 2021. Observation, reminders and follow-up action were proposed</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>and monitored by the ET on handling the wastewater generated from piling works and site surface run-off. Moreover, EPIs from EPD conducted the site inspection on 9th and 29th September 2021. The two inspections conducted by the EPIs focused on reviewing the general site condition, wastewater treatment facilities set-up, mitigation measures for preventing muddy water formation, handling the wastewater and surface run-off. Observations, recommendations and reminders proposed by the EPIs and ET are grouped and shown in Appendix M.</p> <p>Rectification has been reported by the Main Contractor according to the observations and recommendations from ET and EPIs on 8th, 17th, 27th September and 6th October 2021. During the 2nd joint site inspection, EPIs agreed the piling works can be restarted. However, EPIs reminded that the 2nd piling machine can only be operated until the 2nd WetSep is functioning properly and the effluent quality is acceptable. EPIs mentioned that follow-up inspection is expected to be conducted in early or mid-October, focusing on inspecting the wastewater treatment efficiency for piling works, paving of the soil surface, mitigation measures for handling the surface run-off. EPIs also mentioned that a surprise inspection may be conducted in the future. According to AECOM, the piling work was restarted on 30th September 2021.</p> <p>According to this incident, the Main Contractor was reminded by ET to analyze and review the efficiency of the wastewater treatment system according to construction activities regularly. The Contractor should provide regular maintenance, water quality testing and related checklists for ET and IEC review during the site inspection. The Main Contractor and related Sub-Contractor were reminded by ET and AECOM that the discharge of effluent needs to fulfill the requirements stated in the Water Discharge License (No. WT00032446 – 2018). AECOM and ET requested the Main Contractor to update the Temporary Drainage Management Plan according to the latest work activities. ET also requested the Main Contractor to update the description of the wastewater mitigation measures inside the Environmental Management Plan (EMP) and Environmental Management Report (EMR) and strictly implement to prevent similar cases from happening in the future.</p>		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				A follow-up site inspection was conducted by the EPIs at Zone 5 south boundary on 26th October 2021. The EPIs reviewed the site condition, treatment efficiency of the temporary wastewater treatment facilities, mitigation measures to prevent muddy water generated from soil surface, discharge points and gullies condition. EPIs commented on the mitigation measure around the discharge point near WetSep TW-WS1. The bunding next to the manhole should be rectified to prevent the inflow of muddy water. EPIs reminded that mitigation measures (such as sandbags and bunding) should be provided for enclosing the area near the piling machine. It is for directing the muddy water into the temporary wastewater treatment system. EPIs also reminded regular maintenance of the temporary wastewater treatment system is needed to ensure the effluent's water quality fulfill the standard of the Water Discharge License.		
EPD ref.: RN25674- 21	28/10/2021	EPD	Noise	<p>A complaint was received by the EPD Regional Office (North) on 28th October 2021. The complainant was concerned about the night-time noise nuisance near Man Wo House, Wo Che Estate from 2:00 to 5:00 a.m. on 25th, 26th and 27th October 2021 (total 3 nights). The complaint was referred from EPD to (ET on 5th November 2021 at 3:35 p.m.</p> <p>The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Enclosure for General Night Works that was issued by the EPD. According to Main Contractor, the construction work activities were carried out during the permitted hours (00:00-05:00) on 25th and 27th October 2021 near Man Wo House (at Zone 4 and 5, NB and SB) and there was no night works on the 26th October 2021. The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included Temporary Traffic Arrangement (TTA) implementation, unloading of fill materials, loading and unloading of the lamppost, precast concrete blocks and generator and site clearance. The Main Contractor reported that no night-time construction work was carried out on 26th October 2021 at Zone 4 and 5.</p> <p>ET checked the Main Contractor has complied with CNP No.: GW-RN0600-21. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers. The Main Contractor was also be reminded to shut down the PMEs' engines when they are not in use. Moreover, only mobile phones and walkie talkies with headphones can be used for communication, and no whistles, horns and loudspeakers can be used during night work activities. The Main Contractor was reminded to pay attention to CNP conditions 3.d.1, 3.d.5, 3.d.13, 4.d.3 and 4.d.4 for using PMEs to carry out loading and unloading activities in the future.		
COM-2021-0257	05/11/2021	1823	Noise	<p>This complaint was received by 1823 (ref: CASE#3-6960147702) on 5th November 2021 at 02:05 a.m. The complainant, Mr Sung concerned about the night-time noise nuisance from concreting near Scenery Court and Tsing Sha Highway. The complaint was referred from AECOM to ET on 8th November 2021 at 9:34 a.m.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0642-21 Road Closure for Sheet Piles Removal and Road Re-construction Works that issued by the EPD. According to Main Contractor, the construction work activities were carried out during the permitted hours (23:00-05:00) on 4th November 2021 near Scenery Court and Hilton Plaza (Zone 1). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included Temporary Traffic Arrangement (TTA) implementation, preparation works for concreting, concreting, cleaning works after concreting and site clearance.</p> <p>ET conducted a regular night-time noise monitoring at all the monitoring stations between 11:00 p.m. to 03:00 a.m. on 4th November 2021 and at NMS1, NMS2, NMS3, NMS4, NMS5A, NMS6A and NMS7 in Zone 1 and 2 which were close to Scenery Court near Tsing Sha Highway. No exceedance case was found during the regular night-time noise impact monitoring measurement.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0642-21. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers. The Main Contractor was reminded to shut down the PMEs' engines when they are not in use. Moreover, only mobile phones and walkie talkies with headphones can be used for communication, and no whistles, horns and loudspeakers can be used during night work activities. The Main Contractor was also be reminded to pay attention to CNP conditions 3.d.1, 3.d.3, 3.d.4 3.d.5, 3.d.7, 3.d.11, 3.d.13, 4.d.6 and 4.d.7 for using PMEs and carry out similar night-time construction work activities in the future.		
EPD ref.: RN25674- 21	17/11/2021	EPD	Noise	This complaint was received by the EPD Regional Office (North) on 17 th November 2021. The complainant concerned about the night-time noise nuisance near Wai Wah Centre from 2:30 to 3:30 a.m. on 17 th November 2021. The complaint was referred from EPD to ET on 19 th November 2021 at 5:56 p.m. The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0600-21 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) on 16 th and 17 th November 2021 near Wai Wah Centre (Zone 2). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included Temporary Traffic Arrangement (TTA) implementation, unloading and handling of asphalt during pavement, asphalt compaction, loading and unloading of materials and site clearance. ET conducted a regular night-time noise monitoring at all the monitoring stations between 11:00 p.m. to 03:00 a.m. on 18 th and 19 th November 2021 and at NMS1, NMS2, NMS3, NMS4, NMS5A, NMS6A and NMS7 at Zone 1 and 2 which were close to Wai Wah Centre. No exceedance case was found during the regular night-time noise impact monitoring measurement. ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, construction time period, PMEs type and groups and mitigation measures. While prior notification was send to EPD on 12 th November 2021 and Notice to Affected Residents – PN162	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				have been issued to nearby NSRs on 27 th October 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.		
COM-2021-0262	20/11/2021	1823	Noise	<p>This complaint was received by 1823 (ref: CASE#3-6981794553) on 20th November 2021 at 3:35 a.m. The complainant, Mr Sung concerned about the night-time noise nuisance from road surfacing works near Hilton Plaza. The complaint was referred from AECOM to ET on 23rd November 2021 at 1:56 p.m. The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0600-21 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) on 19th and 20th November 2021 near Hilton Plaza (Zone 1 and 2). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included Temporary Traffic Arrangement (TTA) implementation, asphalt removal, unloading and handling of asphalt during pavement, asphalt compaction, loading and unloading of materials and site clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, construction time period, PMEs type and groups and mitigation measures. While prior notification was send to EPD on 12th November 2021 and Notice to Affected Residents – PN162 have been issued to nearby NSRs on 27th October 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs.</p>	Project Related	Closed
COM-2021-0263	26/11/2021	1823	Noise	<p>This complaint was received by 1823 (ref: CASE#3-6991122920) on 26th November 2021 at 11:31 a.m. The complainant, Mr Chan concerned about the night-time noise nuisance generated from road surfacing works at Tai Po Road and near Shing Mun Tunnel Road (Zone 1 and 2). The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Closure for General Night Works that issued by the EPD. The night-time construction works included TTA implementation, asphalt milling, mobilization in</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				and out of construction site, asphalt paving, compaction of asphalt pavement, loading and unloading of fill materials, and site clearance. ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, constriction time period, PMEs type and groups and mitigation measures. While prior notification was send to EPD on 19 th November 2021 and Notice to Affected Residents – PN162 have been issued to nearby NSRs on 27 th October 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs.		
COM-2021-0264	24/11/2021	1823	Noise	<p>This complaint was received by 1823 (ref: CASE#3-6989137345) on 25th November 2021 at 30th November 2021 at 9:28 a.m. The complainant, Ms Sun concerned about the recent noise nuisance from the night-time construction work activities near Sha Tin Station.</p> <p>The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Closure for General Night Works. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) on 23rd^24th November 2021 near Sha Tin Station (at Zone 2). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included Temporary Traffic Arrangement (TTA) implementation, asphalt milling, asphalt paving, compaction of asphalt pavement, loading and unloading of materials, and site clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, constriction time period, PMEs type and groups and mitigation measures. While prior notification was send to EPD on 19th November 2021 and Notice to Affected Residents – PN162 have been issued to nearby NSRs on 27th October 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.</p>	Project Related	Closed
COM-2021-0265	01/12/2021	1823	Noise	This complaint was received by 1823 (ref: CASE#3-6997727629) on 1 st December 2021 at 11:50 a.m. The complainant concerned about the night-time	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>noise nuisance generated near Sha Tin Station.</p> <p>The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Closure for General Night Works. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) on 30th November ^ 1st December 2021 near Sha Tin Station (at Zone 2). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included TTA implementation, asphalt milling, asphalt paving, compaction of asphalt pavement, painting of road marking, loading and unloading of materials, and site clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, constriction time period, PMEs type and groups and mitigation measures. While prior notification was sent to EPD on 19th November 2021 and Notice to Affected Residents – PN162 and 165 have been issued to nearby NSRs on 27th October and 29th November 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.</p>		
EPD ref.: RN29574- 21	07/12/2021	EPD	Noise	<p>This complaint was received by the EPD Regional Office (North) on 7th December 2021. The complainant concerned about the night-time noise nuisance generated from the operation of PMEs near Lek Yuen Estate, Kwai Wo House on 7th December 2021 at 2:00-3:00 a.m.</p> <p>The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Closure for General Night Works. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) on 6th7th December 2021 near Kwai Wo House (at Zone 3). The construction activities were carried out within the allowable location and within the site boundary listed in the CNP. The night-time construction works included TTA implementation, lifting of steel truss of overhead height restriction gantry, installation of overhead height restriction gantry, and site clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, constriction time period,</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				PMEs type and groups and mitigation measures. While prior notification was sent to EPD on 19 th November 2021 and Notice to Affected Residents – PN165 have been issued to nearby NSRs on 29 th November 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.		
COM-2021-0272	16/12/2021	1823	Noise	A complaint was received by 1823 (ref: CASE # 3-7020268390) on 16 th December 2021 at 12:27 a.m. The complainant concerned about the night-time noise nuisance generated from the Tai Po Road (Sha Tin Section) construction site (near Wai Wah Centre, Block 3) in recent days. The construction work activities were allowed under the in-force CNP no.: GW-RN0600-21 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction work activities were carried out during the permitted hours (22:00-05:00) between 13 th and 16 th December 2021 (at Zone 2). The night-time construction works included TTA implementation, asphalt removal and cutting works, loading and unloading of materials, lifting steel plate and site clearance. ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0600-21 about the allowable location, constriction time period, PMEs type and groups and mitigation measures. While prior notification was sent to EPD on 10 th December 2021 and Notice to Affected Residents – PN165 have been issued to nearby NSRs on 29 th November 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.	Project Related	Closed
COM-2021-0193 and COM-2021-0202	21/12/2021	1823	Noise	Three complaints were received by 1823 from the same complainant (ref: CASE # 3-6727963845 via email) on 21 st December 2021 at 8:35 a.m., 22 nd December 2021 at 9:18 a.m. and 5:06 p.m. The complainant, Ms. So concerned about the recent day-time noise nuisance generated from day-time construction works from the Tai Po Road (Sha Tin Section) construction site (near Mei Wo House, Wo Che Estate). According to the Main Contractor, the construction works were carried out at	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>day-time (08:00-18:00) between 15th and 22nd December 2021 near Mei Wo House (at Zone 5). The construction work activities included formwork erection, formwork removal, rebar fixing, and concreting works.</p> <p>ET carried out regular day-time noise monitoring on 20th and 21st December 2021 at NMS 16-20 and NMS 26, no exceedance case was found. All the noise monitoring results at the above-mentioned stations were lower than the noise limit of 75 dB(A) Leq (30 minutes) at the facade of dwellings and 70 dB(A) Leq (30 minutes) for school.</p> <p>To minimize the noise impact generated from day-time construction works, the Main Contractor reported that they have implemented an additional noise mitigation measure (with temporary noise barriers) for the Mei Wo House, NSR. During the ET weekly environmental inspection on 13th January 2022, the noise barriers were observed as properly installed. Most of the sight from the nearby NSRs for the noise works and PMEs were blocked by the implemented noise barrier. There is no particular observation about the noise impact generated from the construction activities during the site inspection. ET reminded the Main Contractor to ensure the additional noise barriers were applied properly next to the PMEs and noisy work. The contractor should minimize the noise impact generated from the daily construction works activities as much as possible.</p>		
COM-2021-0275	29/12/2021	1823	Noise	<p>Two complaints were received by 1823 (ref: CASE # 3-7043757669 via voice mail) on 29th December 2021 at 12:07 a.m. and (ref: CASE # 3-7046572787 via email) on 29th December 2021 at 1:07 a.m. and 1:18 a.m. (repeat email). The complainant, Mr. Sung concerned about the night-time noise nuisance generated from the Tai Po Road (Sha Tin Section) construction site (near Hilton Plaza) on 23rd December 2021 at 12:30 a.m. and 29th December 2021 at 12:00 a.m.</p> <p>According to Main Contractor, there were night-time construction works carried out at Tai Po Road and near Hilton Plaza (Zone 1 and 2) on 22nd ^ 23rd and 28th ^ 29th December 2021. The works included TTA implementation, pavement breaking along existing profile barriers, excavation (handling of rubble), remove steel plate from the trench, pipe laying inside the trench, reinstate steel plate to cover trench, removal of rubble, plant demobilization, and site clearance on 22nd</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>^ 23rd December 2021. Moreover, TTA implementation, dismantling of access tower, noise barrier steel post delivery, plant mobilization, pavement breaking along existing profile barriers, erection of noise barrier steel post, removal of existing profile barriers, and site clearance were carried out on 28th ^ 29th December 2021.</p> <p>ET checked that the Main Contractor did not comply with the conditions listed in CNP No.: GW-RN0600-21 and GW-RN0916-21 during the construction work activities on 22nd ^ 23rd and 28th ^ 29th December 2021 with unauthorized PME being used on-site. Enhance measures and supervision was urged by ET to the Main Contractor to prevent similar incident from happening again. The Main Contractor reported that enhancement measures, included altering the works schedule, enhance supervision and control system are applied currently.</p> <p>The Main Contractor was reminded again by ET to strictly follow and fully comply with the requirement listed in the CNP. Only allowable PMEs listed in the CNP can be used to carry out construction works. Mitigation measures should also be applied according to CNP condition 3.d., 4.d and EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>		
EPD ref.: RN1596-22	17/01/22	EPD	Noise and Dust	<p>The complaint was received by EPD Regional Office (North) (ref: RN1596-22) on 17th January 2022. The complainant who lived near Mei Wo House, Wo Che Estate concerned about the night-time noise and dust nuisance generated from the nearby road.</p> <p>The construction work activities were allowed under the in-force CNP no.: GW-RN0916-21 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction work activities were carried out during the permitted hours (23:00-05:00) on 13th ^ 14th and 14th ^ 15th January 2022 (at Zone 5), and these construction activities were carried out within the allowable location listed in the CNP (Zone I). The night-time construction works on 13th ^ 14th January 2022 included TTA implementation, Loading and Unloading of rubble, Lifting Operation, and Site Clearance. For 14th ^ 15th January 2022, night-time works included TTA implementation, Loading and Unloading of</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>rubble, Lifting operation, Plant mobilization, and Site Clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions in CNP No.: GW-RN0916-21 about the allowable location, constriction time period, PMEs type and groups and mitigation measures. While prior notification was sent to EPD on 7th December 2021 and Notice to Affected Residents – PN162 and 165 have been issued to nearby NSRs on 28th December 2021. The Main Contractor was reminded to pay attention to CNP conditions and minimize the noise nuisance to the nearby NSRs when carry out similar night-time construction work activities in the future.</p>		
COM-2022-0313	08/06/22	1823	Noise	<p>A complaint was received via 1823 (ref: CASE#3-7246071575) on 8th June 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near Wo Che Estate.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0185-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours (23:00-05:00) on 7th June 2022. (At Zone 5). The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP. The night-time construction works on 7th June 2022 included Temporary Traffic Arrangement (TTA) implementation, Erection of noise barrier panels and site clearance.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0185-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed
COM-2022-320	01/08/22	1823	Dust & Noise	<p>A complaint was received by 1823 (ref: CASE#3-7318357344) on 25th July 2022. The complainant who is concerned about the dust and noise nuisance generated from construction works near Shatin Plaza. According to the Main Contractor, there were construction activities near</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				Shatin Plaza (Zone 3) on 25th July 2022. Thus, this complaint considered to be related to the project. According to ET investigation, no exceedance cases were found on ET regular day-time noise monitoring. The Main Contractor was reminded to provide noise mitigation measures for the PMEs and noisy works to ensure the noise impact generated from the site is minimized. Consider the dust nuisance, no exceedance cases were found on ET regular air quality monitoring. The Main Contractor was reminded to provided dust suppression mitigation measures for the exposed area.		
COM-2022-326	05/08/22	1823	Noise	<p>A complaint was received by 1823 (ref: CASE#3-7328538008) on 5th August 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works along Tai Po Road between 3 to 4 a.m.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0476-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours (23:00-04:45). The construction activities were carried out within the allowable location (Zone I, II & III) and within the site boundary listed in the CNP.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0476-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>ET carried out regular night-time noise monitoring on 4th ^ 5th August</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				2022, no exceedance case was found.		
COM-2022-327	05/08/22	1823	Noise	<p>A complaint was received by 1823 (ref: CASE#3-7333891394) on 5th August 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near Lucky Plaza. The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0476-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours (23:00-04:45). The construction activities were carried out within the allowable location (Zone II) and within the site boundary listed in the CNP.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0476-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>ET carried out regular night-time noise monitoring on 4th ^ 5th August 2022, no exceedance case was found.</p>	Project Related	Closed
COM-2022-346	28/10/22	1823	Noise	<p>A complaint was received by the EPD (EPD ref.: RN23746-22) on 28th October 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near King Wo House.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>permitted hours. The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP. ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>ET carried out regular night-time noise monitoring on 27th ^ 28th October 2022 at NMS 26, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p>		
COM-2022-348	4/11/22	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7460684431) on 4th November 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near Sha Tin Plaza.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone II) and within the site boundary listed in the CNP.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.		
COM-2022-349	8/11/22	EPD	Noise	<p>A complaint was received by the EPD (EPD ref.: RN23746-22) on 8th November 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near King Wo House.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP. ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed
COM-2022-350	10/11/22	1823	Water	<p>A complaint was received by the 1823 (CASE#3-7469563820) on 10th November 2022. The complainant who is concerned about muddy water discharged from the construction site to the carriageway near New Town Plaza.</p> <p>According to the Resident Engineer, site personnel discovered the freshwater hose pipe was burst at Site Access N09 at 1:30 p.m. Water spilt in the works area and overflow to the carriageway. The watermain valve was closed by the contractor at 1:45 p.m. and completed replaced</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>the damaged hoes pipe at around 3:00 p.m. According to the Resident Engineer, no muddy water and mud were deposited on the carriageway around the site Access N09. ET checked that the case was a burst of freshwater hose and there was no untreated muddy water discharge was found from the construction site.</p>		
COM-2022-351, COM-2022-352	13/11/22	1823	Noise	<p>Two complaint was received by the EPD (EPD ref.: RN25243-22, RN25259-22) on 13th November 2022. The complainants who are concerned about the noise nuisance generated from night-time construction works near Tai Po Road next to Sha Tin MTR Station. The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone II & III) and within the site boundary listed in the CNP.</p> <p>ET carried out regular night-time noise monitoring on 10th ^ 11th November 2022 at NMS5A, NMS6A, NMS8, NMS9 and NMS24, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
COM-2022-353	17/11/22	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7478880132) on 17th November 2022. The complainants who are concerned about the noise nuisance generated from night-time construction works near Sha Tin Rural Committee Road.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone II) and within the site boundary listed in the CNP.</p> <p>ET carried out regular night-time noise monitoring on 15th ^ 16th November 2022 at NMS8, NMS9, NMS24 and NMS25A, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed
COM-2022-354	17/11/22	EPD	Noise	<p>A complaint was received from EPD (EPD ref: RN25860-22) on 17th November 2022. The complainants who are concerned about the noise nuisance generated from night-time construction works near Wo Che Estate (between Man Wo House and Mei Wo House).</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP. ET carried out regular night-time noise monitoring on 15th ^ 16th November 2022 at NMS19, and NMS20, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>		
COM-2022-356, COM-2022-357, COM-2022-358	29/11/22	1823	Noise	<p>Three complaints were received by 1823 (CASE#3-7495426348, CASE#3-7495543588, CASE#3-7495866890) on 29th November 2022. The complainants who are concerned about the noise nuisance generated from night-time construction works near Tai Po Road. The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP.</p> <p>ET checked that the Main Contractor did not comply with the conditions</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>3.d.19 and 4.d.9 listed in CNP No.: GW-RN0848-22.</p> <p>To discuss the enhancement measures, enhance supervision and control system, an ad-hoc meeting was carried out on 13 December 2022 with the CEDD, ER, IEC, Contractor and ET.</p> <p>A presentation for enhancement measures and enhance supervision was carried out by the contractor on 16 December 2022 with the ER and ET.</p> <p>According to the Main Contractor, to prevent further submission delay, the notification will be notified to the EPD within two consecutive weeks on the Friday of previous working week.</p>		
COM-2022-359	14/12/22	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7516169709) on 14th December 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near Tai Po Road next to the Shatin Plaza.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone II) and within the site boundary listed in the CNP.</p> <p>ET carried out regular night-time noise monitoring on 13th ^ 14th December 2022 at NMS8, and NMS24, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.		
COM-2022-364	20/12/22	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7523479466) on 20th December 2022. The complainant who is concerned about the noise nuisance generated from night-time construction works near Tai Po Road next to the Citylink Plaza on 2 December 2022 at 2:00 a.m.</p> <p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0848-22 Road Closure for General Night Works that issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone II) and within the site boundary listed in the CNP.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0848-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed
COM-2023-376	18/01/23	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7559583506) on 18th January 2023. The complainant who is concerned about the noise nuisance generated from day time construction works near Tai Po Road.</p> <p>The complainant is concerned about the noise nuisance generated from the day-time construction works activities near Tai Po Road at Zone 5 on 18th January 2023 at 7:00 a.m. to 8:00 a.m.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>According to Main Contractor and AECOM's information, there was no construction work undertaken near the concerned area from 7:00 a.m. to 8:00 a.m.</p> <p>ET checked that the complaint received on 18th January 2023 is non-project related.</p>		
COM-2023-382	31/01/23	EPD	Noise	<p>A complaint was received from the EPD (EPD ref.: RN2643-23) on 2nd February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road near the Fo Tan Road from 1:00 a.m. to 3:00 a.m. on 31st January 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to unload the material at a lower level into the dump truck to ensure the noise generated is as low as possible.</p>	Project Related	Closed
COM-2023-383	01/02/23	EPD	Noise	<p>A complaint was received from EPD (EPD ref.: RN2721-23) on 1st February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road next to Wo Shun House and Fung Wo Estate from 12:00 a.m. to 2:00 a.m. on 1st February 2023.</p> <p>According to Main Contractor, the night-time construction works included plant mobilization, loading and unloading construction material and</p>	Non-Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>loading and unloading C&D waste material were carried out between 31st January and 1st February 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>ET carried out regular night-time noise monitoring on 31st January ^ 1st February 2023 at NMS26, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>The Main Contractor was reminded to unload the material at a lower level into the dump truck to ensure the noise generated is as low as possible.</p>		
COM-2023-384	6/2/23	1823	Wastewater	<p>A complaint was received by the 1823 (CASE#3-7578244130) on 6th February 2023. The complainant who is concerned about wastewater discharged from the construction site to the Tai Po Rad carriageway on 4th February 2023.</p> <p>According to the Main Contractor, the water was from emptying the water barriers and flowed outside the site without washing dirt and mud.</p> <p>ET checked that no untreated wastewater was discharge to the carriageway.</p> <p>The main contractor is reminded to provide more training to the frontline staff to ensure no more water will be direct discharge from the construction site.</p> <p>The main contractor is reminded that surface run-off should be prevented from directly entering the sensitive receivers during the construction works.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				The main contractor is reminded that the wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged.		
COM-2023-385	14/2/23	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7591662478) on 14th February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road next to Wo Che Estate.</p> <p>According to the Main Contractor, the night-time construction works included TTA implementation, loading and unloading, pouring non-fine concrete and asphalt paving were carried out between 13th and 14th February 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>According to AECOM, the acoustic barrier was not fully used during the whole process of road paving. The Main Contractor was reminded to use the acoustic barrier for blocking the power generating part of the PME to ensure the noise can be minimized.</p>	Project Related	Closed
COM-2023-386	20/2/23	Contract Hotline Phone Call	Noise	A complaint was received by Contract Hotline Phone Call (COM-2023-0386) on 20th February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>near Tai Po Road next to Wo Che Street between 17th and 18th February 2023 from 0:00 to 04:00 a.m.</p> <p>According to the Main Contractor, the night-time construction works included TTA implementation, loading and unloading and site clearance were carried out between 17th and 18th February 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to be slow and careful when carrying out loading and unloading to avoid remarkable noise nuisance.</p>		
COM-2023-387	24/2/23	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7605775385) on 24th February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road next to Wo Che Estate.</p> <p>According to the Main Contractor, the night-time construction works included TTA implementation, loading and unloading, pouring non-fine concrete and asphalt paving were carried out between 20th and 24th February 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>ET carried out regular night-time noise monitoring on 23rd ^ 24th February 2023 at NMS19, and NMS20, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p>		
COM-2023-388	25/2/23	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7608102288) on 25th February 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road on 25th February 2023 from 4 a.m. to 5 a.m.</p> <p>According to the Main Contractor, the night-time construction works included plant mobilization and site clearance were carried out on 25th February 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed
COM-2023-392 and 393	2/3/2023	CEDD	Noise	<p>Two complaints were received from CEDD (COM-2023-392 and 393) on 2nd March 2023. The complainants are concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road next to Man Wo House.</p> <p>According to the Main Contractor, the night-time construction works included TTA implementation, loading and unloading, noise barrier installation, asphalt milling, asphalt paving and site clearance were carried out on 2nd March 2023.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>According to the Main Contractor, the road miller, asphalt paver and road roller were used behind acoustic barriers when road paving works was carrying out. Also, the internal sound absorbing lining was installed for those engine compartments.</p> <p>According to the Main Contractor, the soft padding material was padded on the ground when loading and unloading the steel rebars.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-394	9/3/2023	EPD	Noise	<p>A complaint was received from EPD (EPD ref.: RN6366-23) on 9th March 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road from 1 a.m. to 4 a.m.</p> <p>According to the Main Contractor, the night-time construction works</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>included TTA implementation and loading and unloading were carried out on 9th March 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to be slow and careful when carrying out loading and unloading to avoid remarkable noise nuisance.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-395	14/3/2023	EPD	Noise	<p>A complaint was received from EPD (EPD ref.: RN6778-23) on 14th March 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road on 14th March 2023 from 2 a.m. to 3 a.m.</p> <p>According to the Main Contractor, the night-time construction works included loading and unloading were carried out on 14th March 2023 from 2 a.m. to 3 a.m.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to be slow and careful when carrying out loading and unloading to avoid remarkable noise nuisance.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-402	18/3/2023	Contract Hotline	Noise	<p>A complaint was received by contract hotline (COM-2023-402) on 18th March 2023. The complainant is concerned about the noise nuisance generated by placing traffic cones on Tai Po Road during night-time construction activities on 18th March 2023.</p> <p>According to the Main Contractor, all workers were briefed before the works started. The workers were reminded the traffic cones must be put on the ground, rather than throwing.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to place the traffic cones slowly and</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>carefully to minimize the noise nuisance generated.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-403	18/3/2023	1823	Noise	<p>Two complaints were received by 1823 (CASE#3-7637259453 & #3-7637259880) on 18th March 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Tai Po Road on 18th March 2023.</p> <p>According to the Main Contractor, no Power Mechanical Equipment was included in the relevant complainant cases on 18th March 2023.</p> <p>Referring to the complainant's video, the noise was generated when the frontline workers threw the materials from a height to the ground. In addition, the contractor's mitigation measure is not enough to minimize the noise generated. The Main Contractor was reminded to provide more training for frontline workers to ensure that they work with minimum noise.</p> <p>According to the Main Contractor, a night-work foreman was arranged to keep close monitoring the noisy work and ensure the compliance of CNP at night.</p> <p>The Main Contractor was reminded to unload all the construction materials slowly and carefully to minimize the noise generated.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN1176-22. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-404	18/3/2023	1823	Wastewater	<p>A complaint was received by 1823 (CASE#3-7637522160) on 18th March 2023. The complainant is concerned about the wastewater leaking from the STRCR to the below carriageway.</p> <p>The complainant who is concerned about the wastewater leaking into the carriageway surface from STRCR on 18th March 2023.</p> <p>ET checked that the complaint was considered to be related to the project.</p> <p>According to the Main Contractor, the dripping was caused by the concrete curing work above the STRCR structure.</p> <p>According to the Main Contractor, the drip source reparation work was conducted on 20th March and completed on 26th March 2023. No more drip source was observed.</p> <p>During the site inspection, ET checked the main contractor had used the tarpaulin sheet as the mitigation measure of the concrete curing work. The Main Contractor was reminded to periodic inspection the site situation to ensure the mitigations are effective.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>The Main Contractor was reminded that the run-off should be prevented from directly entering the sensitive receivers during the construction works.</p> <p>The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged.</p>		
COM-2023-406	23/3/2023	1823	Wastewater	<p>A complaint was received by 1823 (CASE#3-7616071795) on 23rd March 2023. The complainant is concerned about the wastewater leaking to the drainage system.</p> <p>The complainant who is concerned the wastewater discharged to the drainage system on the carriageway road.</p> <p>ET checked that the complaint was considered to be related to the project.</p> <p>According to the Main Contractor, the water was the result of the excessive curing water seeped underneath the STRCR flyover. The dripping ceased shortly. Due to the small quantity and short time, the dripping did not constitute a continuous flow.</p> <p>According to the Main Contractor, the drip source was repaired on 26 March 2023. No more drip source was observed.</p> <p>During the site inspection, ET checked the main contractor had used the tarpaulin sheet as the mitigation measure of the concrete curing work.</p> <p>ET checked no wastewater was discharged at the concerned area after the reparation work.</p> <p>The Main Contractor was reminded that the run-off should be prevented from directly entering the sensitive receivers during the construction works.</p> <p>The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				discharge license before being discharged.		
COM-2023-411	18/4/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7677865059) on 18th April 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Tai Po Road.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction work should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>	Project Related	Closed
COM-2023-412	28/4/2023	EPD	Noise	<p>The construction work activities were allowed under the in-force Construction Noise Permit (CNP) no.: GW-RN0292-23 Road Closure for General Night Works issued by the EPD. According to the Main Contractor, the construction works activities were carried out during the permitted hours. The construction activities were carried out within the allowable location (Zone I) and within the site boundary listed in the CNP. According to the Main Contractor, the night-time construction works included TTA implementation, Loading & unloading, Asphalt Milling, Asphalt Paving and Concreting were carried out between 20th and 25th</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>April 2023.</p> <p>According to the Main Contractor, no construction works were carried out between 23rd and 24th April 2023.</p> <p>According to AECOM information, only housekeeping was carried out on 23rd ^ 24th April 2023. No major construction work was recorded on Sunday.</p> <p>The Environmental Officer reported that a prior notification was sent to EPD on 13th April 2023 at 02:08 p.m. and 20th April 2023 at 01:48 p.m. While "Notice to Affected Residents – PN240" was sent to the Sha Tin District Council, Local Residents, Private Development and Others on 29th March 2023.</p> <p>ET carried out regular night-time noise monitoring on 20th ^ 21st April 2023 at NMS16, NMS18, NMS19, NMS20 and NMS26, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction work should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out</p>		

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				similar night-time construction work activities in the future.		
COM-2023-502	12/5/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7709231017) on 12th May 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Tai Po Road.</p> <p>ET carried out regular night-time noise monitoring on 9th ^ 10th May 2023 at NMS9 and NMS13, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>	Project Related	Closed
COM-2023-503	19/5/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7722776885) on 19th May 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Tai Po Road.</p> <p>According to the Main Contractor, additional temporary noise barriers will</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>be provided as an enhancement noise mitigation measure.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0514-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6 and 3.d.7 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-504	14/5/2023	EPD	Noise	<p>A complaint was received from EPD (EPD ref.: RN12170-23) on 14th May 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Lek Yuen Estate after 7:00 p.m.</p> <p>According to the Main Contractor and AECOM information, no construction works were carried out between 19:00 and 22:00. Also, no construction works were carried out at Zone 3 on 12th ^13th May 2023.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23 and CNP no. GW-RN0227-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PME's listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PME's and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
COM-2023-510	30/6/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7780620261) on 30th June 2023. The complainant is concerned about the noise nuisance generated by the night-time construction works activities near Wai Wah Centre. According to the Main Contractor, all crane lorry and dump truck drivers were briefed to load all material at the lower level to minimize noise generation.</p> <p>ET carried out regular night-time noise monitoring on 29th ^ 30th June 2023 at NMS5A, NMS6A and NMS8, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				<p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>		
CASE# 3-778274445 4	3/7/2023	1823	Noise	<p>A complaint was received by 1823 (CASE# 3-7782744454) on 3rd July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Jockey Club Ti-I College.</p> <p>Due to the distance of the concerned area is far from the construction site, the complaint was considered to be non-project related.</p> <p>ET carried out regular night-time noise monitoring on 29th ^ 30th June 2023 at NMS19, no exceedance case was found. All the noise monitoring results at the above-mentioned station were lower than the limit level (55 dB(A)).</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
				The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.		
EPD ref. RN14897-23	7/7/2023	EPD	Noise	<p>A complaint was received by EPD (EPD ref. RN14897-23) on 7th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Scenery Court. According to the Main Contractor, no construction activities were carried out near Scenery Court. The nearest activities were carried out near Wai Wah Centre. Due to the certain distance between the working area and the concerned area, this complaint was considered to be non-project related.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0292-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PMEs listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PMEs and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
EPD ref.: RN16920- 23	19/7/2023	EPD	Noise	<p>A complaint was received by EPD (EPD ref.: RN16920-23) on 19th July 2023. The complainant who is concerned about the untreated muddy water discharged from the construction site to the Shing Mun River. According to the government's info-map, the drainage network of the concerned water outfall is distributed along the Wo Che Street and construction site area Zone 4 is also covered in the network. According to the Main Contractor, all the work activities were operated with suitable water treatment facilities and no water discharged between 11th July 2023 14th July 2023. According to AECOM photo records on 12th July 2023, a small amount of muddy water leakage through the sandbag bunding into the manhole at Zone 4 was observed. However, the leakage is not sufficient to form the muddy water discharge at Shing Mun River. The Main Contractor was reminded to periodic inspection the site situation to ensure all the mitigation measures are effective. The Main Contractor was reminded that the run-off should be prevented from directly entering the sensitive receivers during the construction works. The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged. ET checked that there is no sufficient evidence to prove that the complaint is related to the project.</p> <p>complaint was received by 1823 (CASE#3-7677865059) on 26th July 2023.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
CASE#3-7677865059	26/7/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7677865059) on 26th July 2023. The complainant who is concerned about the noise nuisance generated from night-time construction works near Sui Wo Court. According to the Main Contractor, the hand-held breaker was used inside the acoustic enclosure.</p> <p>According to the Main Contractor and AECOM, acoustic barriers were set up in the direction of Wo Che Estate during the construction activities. However, due to the safety reason, the noise barriers cannot set up in the direction of Sui Wo Court.</p> <p>According to the Main Contractor, refreshment training will be provided to the frontline supervisory staff about the CNP requirements to ensure all the construction activities fulfil all the conditions in the CNP.</p> <p>ET checked that the Main Contractor had complied with the conditions listed in CNP No.: GW-RN0627-23. The Main Contractor was reminded to strictly follow and fully comply with the requirement listed in the CNP and the mitigation measures stipulated in the EM&A Manual when carrying out construction activities during the restricted hour. All construction works should be carried out as quickly as possible to minimize the noise nuisance to the sensitive receivers.</p> <p>The Main Contractor was reminded to use the allowable PME's listed in CNP condition 3.d for performing night-time construction works. Mitigation measures need to be applied according to the requirement in conditions 3.d and 4.d.</p> <p>The Main Contractor was also be reminded to pay attention to CNP conditions 3a, 3.d.1, 3.d.5, 3.d.6, 3.d.7 and 3.d.14 for using PME's and need to provide related noise mitigation measures when carrying out similar night-time construction work activities in the future.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Reference No.	Date of Complaint Received	Received From	Nature of Complaint	Investigation/Mitigation Action	Outcome	Status
CASE#3-7875615750	31/8/2023	1823	Noise	<p>A complaint was received by 1823 (CASE#3-7875615750) on 31st August 2023. The complainant who is concerned about the muddy water flooded out of the construction site.</p> <p>According to the Main Contractor, the muddy water overflow was the result of the frequent rainstorms that occurred.</p> <p>ET checked that the complaint was considered to be related to the project.</p> <p>The Main Contractor was reminded to provide a site channel, bunds or sandbags as a direct runoff into the sediment traps to prevent muddy water directly discharged to the public area.</p> <p>The Main Contractor was reminded to periodic inspections of the site to determine compliance with the functioning of onsite surface water collection channels and sediment traps.</p> <p>The Main Contractor was reminded to review all the capacity of sedimentation tanks on the site to see if they are enough to handle the heavy rain situation.</p> <p>The Main Contractor was reminded that all wastewater generated on-site should be collected and treated to meet the requirements of the discharge license before being discharged.</p>	Project Related	Closed

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Cumulative Statistics on Complaints

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints in the Reporting Period			Cumulative Project-to-Date
		Jun 2023	Jul 2023	Aug 2023	
Air	7	0	0	0	7
Noise	75	1	3	0	79
Water	7	0	1	1	9
Waste	0	0	0	0	0
Total	89*	1	4	1	95*

*The 1st complaint in March 2021, Jan 2022 and July 2022 were included both the air and noise parameters, hence the total no. of complaints is deducted by 2.

Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Reporting Period			Cumulative Project-to-Date
		Jun 2023	Jul 2023	Aug 2023	
Air	0	0	0	0	0
Noise	1	0	0	0	0
Water	0	0	0	0	0
Waste	0	0	0	0	0
Total	1	0	0	0	0

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix G

Environmental Mitigation Implementation Schedule (EMIS)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
<u>Noise Measures</u>				
3.10.2, 3.10.3, 3.10.14, 3.10.15 and Table 3.10	Within the boundaries of all construction sites.	• Scheduling the construction activities carefully according to the actual site work situation, avoid of concurrent activities and construction works fronting the affected schools, to minimize the total noise generated (max as 102dB (A)).	Contractor	Implemented
		• PME is recommended to operate in sub-grouping, and different sub-groups shall not be operated concurrently within any half hour period	Contractor	Implemented
		• The construction activities should be carried out in the daytime hours (0700 – 1900). Construction Noise Permit (CNP) for construction activities is required during evening or night time hours.	Contractor	Implemented
		• Construction work programme should be considered before actual construction work is undertaken, and noise mitigation measures should be implemented to minimize the potential construction noise impact. Selection and optimization of construction programmes, avoidance and reduction of parallel operation of noisy PME during noise sensitive periods.	Contractor	Implemented
		• Use of well-maintained and regularly-serviced plant during the works.	Contractor	Implemented
		• Plant operating on intermittent basis should be turned off or throttled down when not in active use.	Contractor	Implemented
		• Plant that is known to emit noise strongly in one direction should be orientated to face away from the NSRs.	Contractor	Not Applicable
		• Silencers, mufflers and enclosures for plant should be used where possible and maintained adequately throughout the works.	Contractor	Implemented
		• Fixed plants should be sited away from NSRs where possible.	Contractor	Not Applicable
		• Stockpiles of excavated materials and other structures such as site buildings should be used effectively to screen noise from the works.	Contractor	Not Applicable
3.10.4, 3.10.5 and Table 3.3		• The use of particular plant with equipment quieter than those specified in the GW-TM are recommended to reduce the noise levels generated by the plant.	Contractor	Implemented
		• Other type of quiet PME are allowed to use for their needs based on the actual construction conditions and programmes	Contractor	Implemented
3.10.6 to 3.10.9		• Temporary noise barriers provide noise attenuation by screening NSRs from stationary and mobile plants from direct line-of-sight in shadow zone.	Contractor	Implemented
		• The use of 3m high moveable barriers with skid footing and a small cantilevered upper portion should be adopted. The barrier material shall have a surface mass of not less than 14kg/m ² on skid footing with 25mm thick internal sound absorptive lining to achieve the maximum screening effect.	Contractor	Not Applicable

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		• These temporary noise barriers should be located immediately adjacent to working area.	Contractor	Implemented
		• The temporary noise barriers should be located along the working area to make sure the construction plant could be screened during all kinds of construction activities as far as practicable.	Contractor	Not Applicable
		• Noise jacket/muffler shall be used to cover the noisy part of the engine or at the engine exhaust of particular mobile plants respectively when temporary noise barriers are not practicable or noise reduction achieved is insufficient.	Contractor	Implemented
		• For the stationary plant bored pile oscillator, temporary noise barriers of sufficient height with skid footing and small cantilevered upper portion should be provided.	Contractor	Not Applicable
		• Barrier material of surface density of at least 14 kg/m ² is recommended in order to achieve the necessary screening effect.	Contractor	Not Applicable
3.10.10		• Full noise enclosures should cover the PME or fixed plants such as air compressor.	Contractor	Implemented
3.10.3		• Silencers, mufflers and enclosures for plant should be used where possible and maintained adequately throughout the works;	Contractor	Not Applicable
		• Where possible fixed plants should be sited away from NSRs; and	Contractor	Not Applicable
		• Stockpiles of excavated materials and other structures such as site buildings should be used effectively to screen noise from the works.	Contractor	Not Applicable
Air Quality Measures				
4.12.1 and 4.12.2	Within the boundaries of all construction sites.	• The Contractor shall notify any specific construction works as stated in the Air Pollution Control (Construction Dust) Regulation to the Authority before the commencement of such work. Dust mitigation measures stipulated in the Air Pollution Control (Construction Dust) Regulation should be implemented to control dust emissions from all construction work sites.	Contractor	Implemented
		• The Contractor shall undertake at all times to prevent dust nuisance as a result of his activities. Dust suppression measures such as the water spraying are necessary and should be installed to ensure that the air quality at the boundary of the site and at any sensitive receivers complies with the Hong Kong Air Quality Objectives.	Contractor	Implemented
		• The Contractor shall apply for a license or permit under the requirements of the relevant legislation (e.g. Air Pollution Control Ordinance and its subsidiary regulations) wherever applicable.	Contractor	Implemented
		• Watering of unpaved areas, access roads, construction areas and dusty stockpiles shall be undertaken at least eight times daily during dry and windy weather. Watering of the haul road shall be undertaken four to eight times daily during dry or windy weather. Water sprays may be either fixed or mobile to follow individual areas to be wetted as and when required. Application of suitable wetting agents, such as dust suppression chemicals, shall be used in addition to water,	Contractor	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		especially during the dry season (October to December). It is also suggested that watering with complete coverage of active construction area eight times a day.		
		• Effective water sprays shall be used during the delivery and handling of all raw sand and aggregate, and other similar materials, wet dust is likely to be created and to dampen all stored materials during dry and windy weather.	Contractor	Implemented
4.12.1		• Stockpiles of sand, aggregate or any other dusty materials greater than 20m ³ shall be enclosed on three sides, with walls extending above the pile and 1 meter beyond the front of the pile.	Contractor	Partially Implemented
		• Suitable chemical wetting agent such as dust suppression chemical shall be used on completed cuts and fills to reduce wind erosion.	Contractor	Not Applicable
		• Areas within the construction site where there is a regular movement of vehicles shall have a paved surface and be kept clear of loose surface material.	Contractor	Implemented
		• The Contractor shall restrict all motorized vehicles within the construction site, excluding those on public roads, to maximum speed of 20 km per hour and confine haulage and delivery vehicles to designated roadways inside the Site.	Contractor	Implemented
		• Construction working areas should be restricted to a minimum practicable size.	Contractor	Implemented
		• The Contractor shall ensure that no earth, rock or debris is deposited on public or private rights of way as result of his activities, including any deposits arising from the movement of plant or vehicles.	Contractor	Implemented
		• The Contractor shall provide a wheel washing facility at the exits from work areas to the satisfaction of the Engineer and to the requirements of the Commissioner of Police. Water in wheel washing facilities and sediment shall be changed and removed respectively at least once a month.	Contractor	Implemented
		• The Contractor shall submit details of the wheel washing facilities, which shall be usable prior to any earthworks excavation activity on the construction site. The Contractor shall also provide a hard-surfaced road between any washing facility and the public road.	Contractor	Implemented
		• In the event of any spoil or debris from construction works being deposited on adjacent land, or steams, or any slit being washed down to any area, then all such spoil, debris or material and silt shall be immediately removed and the affected land and areas restored to their natural state by the Contractor to the satisfaction of the Engineer.	Contractor	Implemented
		• If spoil cannot be immediately transported out of the Site, stockpiles should be stored in sheltered areas.	Contractor	Implemented
		• Plant and vehicles shall be inspected annually to ensure that they are operating efficiently	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		and that exhaust emissions are not causing a nuisance. All site vehicle exhausts should be directed vertically upwards or directed away from ground.		
4.12.1, 4.13.1 and Table 8.2		•Construction dust monitoring shall be carried out at representative monitoring locations during the construction period.	Contractor	Implemented
		• Path for complaints and handling procedures should be set up and implement.	Contractor	Implemented
NA		• Dark smoke emission shall be control in accordance with the Air Pollution Control (Smoke) Regulation and ETWB TCW 19/2005.	Contractor	Implemented
		• Plant and equipment should be well maintained to prevent dark smoke emission.	Contractor	Implemented
		• Only approved or exempted Non-road Mobile Machineries (NRMMS) including regulated machines and non-road vehicles with proper labels are allowed to be used in specified activities on-site.	Contractor	Partially Implemented
Water Quality Measures				
		• Silt-laden surface run-off should be prevented from directly entering the sensitive receivers during the construction works. The mitigation measures described below for the construction phase are in accordance with ProPECC PN 1/94:	Contractor	Partially Implemented
		• Construction works should be programmed so as to minimise excavation during the wet season (April to September). If this is not possible then measures should be taken to minimise the areas exposed by covering temporary exposed slopes with tarpaulins or similar material, the protection of temporary road surfaces with gravel or crushed stone and the early reinstatement of final surfaces with hydro seed grass/shrub mixture. This latter measure would have the added benefit of reducing the windblown dust during the dry season. Where temporary covering of slopes is required this should be carried out before the onset of the rainfall or storm.	Contractor	Implemented
5.7	Within the boundaries of all construction sites.	• Existing and newly constructed open manholes should be covered and sealed to prevent run off and water borne debris entering the drainage network without having previously passed through a sediment trap.	Contractor	Implemented
		• Stock piles of construction materials, sand and gravel or excavated material should be covered with tarpaulins prior to rainstorms. The washing of material from the stockpiles directly into the storm drains should be prevented by passing the run off through a sediment trap.	Contractor	Implemented
		• The surface water from the site should be discharged into storm water drain after passing through sand and silt traps designed to accommodate the maximum discharge from the site. Within the site channels, bunds or sandbags should be used to direct run off into the traps. Storm water from outwit the site should be prevented from washing over the site by the construction of interceptor channels at the site boundary. Both perimeter channels and the sedimentation traps should be	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		constructed prior to the commencement of site formation and earthworks.		
		<ul style="list-style-type: none"> The efficiency of the interceptor channels, traps and sedimentation chambers should be maintained by regular cleaning of accumulated silt and sand. Particular attention should be paid to maintenance following heavy rainfall and immediately after the issue of heavy rainfall warning by the Hong Kong Observatory. 	Contractor	Implemented
		<ul style="list-style-type: none"> The ingress of rainwater into trenches should be minimised by the construction of bunds to prevent water flowing into the trench and covering by tarpaulins to prevent direct entry. The lengths of excavated trenches should be minimised and backfilled at the earliest opportunity. Water pumped from the trenches should be discharged to the storm water drains following passage through a suitable silt trap. 	Contractor	Implemented
		<ul style="list-style-type: none"> Any ground water seeping into any trenches or foundation works should be passed through a silt trap prior to discharge to the storm water drains. 	Contractor	Partially Implemented
		<ul style="list-style-type: none"> The water used for the washing down of mixing drums used for onsite batching of concrete and delivery lorries for off-site batched concrete should be recycled whenever possible. Wastewater generated from the washing which is discharged should be passed through a silt trap before discharge to the storm water system. 	Contractor	Not Applicable
		<ul style="list-style-type: none"> The wastewater from the washing of the wheels and subframe of vehicles returning from the site onto public roads will contain suspended solids and debris. A washing bay should be provided at the exit from the site and should, where practicable, incorporate water recirculation. Water from the washing bay which is discharged to the storm water system should first be passed through a silt trap which also includes an oil/grease removal weir. 	Contractor	Implemented
		<ul style="list-style-type: none"> Plant maintenance areas should be paved to prevent waste oils soaking into the ground. Where possible the area should be undercover to minimise the formation of runoff and any runoff from the paved area passed through an oil trap before being discharged to the storm drains. Fuel storage tanks should be surrounded by bunds with a capacity of at least 150% of the storage capacity. The bunded areas should be able to be drained of rain water through the petrol interceptor and accumulated rain removed at regular intervals. 	Contractor	Partially Implemented
		<ul style="list-style-type: none"> Waste oils from the site should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance and absorbent cloths and granules should be available for the cleanup of spillages. 	Contractor	Implemented
		<ul style="list-style-type: none"> Sewage from toilets and kitchens should be discharged directly into a foul sewer. If it is not possible to locate the site offices within easy access of a foul sewer a septic tank and soakaway should 	Contractor	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
Section 12.6 of the Approved EIA Report		be constructed before the offices are occupied. Chemical toilets should be emptied on a daily basis and the contents taken to a foul sewer or the Sha Tin Sewage Treatment Works for disposal. Wastewater collected from canteen kitchens should be discharged to the foul sewers via grease traps which provide a minimum of 20 minutes retention during peak flow. All discharges into foul sewers and storm sewers should have to be complied with TM standards under WPCO.		
		• Run off from roofed surfaces of site facilities should be collected and diverted to a storm water drain. Passage through a silt trap is only required if the water is diverted via open channels which might accumulate solids during non-rainy periods or which intercept surface run off from unpaved areas.	Contractor	Not Applicable
		• Discharges from the site shall be required to meet the terms and conditions of a valid WPCO Water Pollution Control Ordinance (WPCO).	Contractor	Partially Implemented
		• Regular site inspection of the construction works shall be carried out to determine compliance with the recommended mitigation measures. Inspection should be included:		
		(i) The functioning of onsite surface water collection channels and sediment traps.	Contractor	Implemented
		(ii) The functioning of interception channels at the boundary of the works areas	Contractor	Implemented
		(iii) The covering of stockpiles of fill and construction materials and the routing of any run off through the sediment traps.	Contractor	Implemented
		(iv) The pumping procedures for emptying trenches and other excavations and the use of silt traps prior to the discharge of the water to the storm water system.	Contractor	Implemented
		(v) The use of washwater for hosing down concrete mixing and delivery vehicles and other vehicles leaving the site and the routine of excess water from the facility through sediment traps.	Contractor	Implemented
		(vi) The operation of the plant maintenance areas to control small spillages and the correct management of the fuel storage bunded area.	Contractor	Implemented
(vii) The connection of the site office wastewater discharge to an existing foul sewer if appropriate or the operation of the kitchen wastewater grease trap and the regular emptying of the chemical toilets	Contractor	Implemented		
(viii) The operation of the roof rain water collection and drainage system.	Contractor	Implemented		
<i>Landscape and Visual Mitigation Measures</i>				
Table 6.5	Construction Phase			

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
	During construction within the Project Boundary.	• Existing trees shall be preserved as much as possible. Detailed tree preservation and transplanting proposals shall be submitted to relevant government departments for approval in accordance with DEVB TC (W) No. 7/2015.	Contractor	Implemented
		• Topsoil will be conserved as far as possible during the road improvement works and utilized during the replanting operations. The stock piling height of the topsoil will not be more than 2m.	Contractor	Implemented
		• Old and valuable trees (OVTs) identified in the Project Boundary shall be protected in accordance with ETWB TCW no. 29/2004.	Contractor	Implemented
		• Night-time lighting glare shall be properly managed and control during construction so as to minimize any adverse visual impact on adjacent VSRs.	Contractor	Implemented
		• Decorative screen hoarding with design compatible with the surrounding landscape setting shall be erected along the southern boundary of Tai Po Road to mitigate any potential adverse impact on adjacent Pedestrian and Cyclists on Footpath/Bicycle Track.	Contractor	Not Applicable
Operation Phase				
	During construction within the Project Boundary.	• Compensatory planting shall be provided within and outside the project boundary where possible. Detailed compensatory planting proposal will be prepared in accordance with DEVB TC (W) No. 7/2015.	Contractor	Not Applicable
		• Planting shall be undertaken at the earliest practical time in the construction period. The planting proposal shall aim to strengthen the existing tree species and supplement the existing tree planting to provide an effective screen to ameliorate any potential landscape and visual impacts. The proposed species to be utilized for road improvement works shall be agreed with LCSD and future maintenance authorities. All the proposed species for compensatory planting shall be suitable for roadside streetscape planting.	Contractor	Not Applicable
		• Provision of visually pleasing noise barriers and enclosures design shall be proposed. The design of these structures aims to minimize any potential visual impact and visually integrate the proposed structures into the adjacent landscape context. This should be achieved through the use of form, color, tones, materials and planting materials.	Contractor	Not Applicable
		• Aesthetically pleasing hard landscape treatment of the carriageway and roadside furniture shall be proposed, including development of chromatic themes in the architectural treatment of engineering structures, and the consideration of landscape lighting and special landscape features.	Contractor	Not Applicable

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		<ul style="list-style-type: none"> Shrubs and climbers planting are proposed on the facade of Noise Enclosures and Barriers to mitigate any adverse impact on adjacent VSRs in area where space for tree planting is not feasible. 	Contractor	Not Applicable
<i>Waste Management Measures</i>				
7.6.2 to 7.6.4	Within the boundaries of all construction sites.	<ul style="list-style-type: none"> In accordance with ETWB TC (W) No. 19/2005 - Environmental Management on Construction Sites", the Contractor shall prepare and implement a Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP). The EMP shall describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval. 	Contractor	Implemented
		<ul style="list-style-type: none"> The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor. 	Contractor	Implemented
7.6.5 to 7.6.6		<ul style="list-style-type: none"> Recommendations of good site practices and waste reduction measures should be stated in order to achieve avoidance and minimization of waste generation in the hierarchy. 	Contractor	Implemented
		<ul style="list-style-type: none"> Environmental Management Plan (EMP) and trip-ticket system shall be implemented for monitoring management of waste. 	Contractor	Implemented
		<ul style="list-style-type: none"> Specific measures targeting the mitigation of impacts in works areas and the transportation of spoil off-site should be provided to minimize the potential impacts to the surrounding environment. 	Contractor	Implemented
7.6.7	Within the boundaries of all construction sites as well as transportation routes to designed areas for off-site disposal	<ul style="list-style-type: none"> To facilitate adoption of the best-practice philosophy, training shall be provided to all personnel working on site. The training shall promote the concept of general site cleanliness and clearly explain the appropriate waste management procedures defined in the EMP. Overall, the training should encourage all workers to reduce, reuse and recycle wastes. 	Contractor	Implemented
7.6.8 to 7.6.9		<ul style="list-style-type: none"> The contractor's environmental performance shall be monitored and controlled through the weekly environmental walks. The items after the environmental walks shall include: 		
		<ul style="list-style-type: none"> A review of the EMP in particular the suitability of the environmental measures on nuisance abatement and waste management adopted by the contractor; 	Contractor	Implemented
		<ul style="list-style-type: none"> The environmental performance of the contractor and his sub-contractors; 	Contractor	Implemented
		<ul style="list-style-type: none"> The effectiveness of the environmental measures on nuisance abatement and waste management implemented on the site, and any complaints received; and 	Contractor	Implemented

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
7.6.10	of materials/Prior to and during construction activities.	<ul style="list-style-type: none"> The promptness of rectification or improvement actions of the Contractor on the defects and deficiencies identified during inspections of the site. 	Contractor	Implemented
		<ul style="list-style-type: none"> Waste shall only be disposed of at licensed sites and the WMP should include procedures to ensure that illegal disposal of wastes does not occur. Only waste haulers authorized to collect the specific category of waste concerned should be employed and a trip ticket system shall be implemented for offsite disposal of inert C&D materials and non-inert C&D materials at public fill reception facilities and landfills, respectively. Appropriate measures should be employed to minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed containers. 	Contractor	Implemented
		<ul style="list-style-type: none"> Work site(s) shall be arranged and managed to facilitate the proper management of wastes and materials. The WMP shall include plans indicating specific areas designated for the storage of particular types of waste, reusable and recyclable materials as well as areas and management proposals for any stockpiling areas. Waste storage areas should be well maintained and cleaned regularly. Specific provisions for different types of material are outlined below. In general, these areas should be designed to avoid cross contamination of materials as well as pollution of the surrounding environment. 	Contractor	Partially Implemented
7.6.11 to 7.6.14		<ul style="list-style-type: none"> In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the excavated fill materials should be reused on site as backfill material as far as possible. 	Contractor	Implemented
		<ul style="list-style-type: none"> Careful design, planning and good site management should be maintained in order to minimise over ordering and generation of surplus materials such as concrete, mortars and cement grouts. The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse. 	Contractor	Implemented
		<ul style="list-style-type: none"> C&D materials should be segregated on site into different waste and material types. The Contractor should clearly demonstrate in the EMP how he intends to maximise the reuse of C&D material on-site. Where reuse of materials on site is not feasible, the Contractor should explore opportunities for recycling materials off-site, and inert C&D materials shall be reused on site as much as possible. 	Contractor	Implemented
		<ul style="list-style-type: none"> Paving bricks arising from existing pavement should be recycled on site as much as possible. 	Contractor	Not Applicable
		<ul style="list-style-type: none"> Existing marginal roadside barriers comprise pre-cast units should be reused in the following widening works as much as possible, 	Contractor	Not Applicable

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		• Existing bridge parapets comprise aluminum post and railings, which have a recyclable value and should be sold for reconditioning or reused for scrap metal as much as possible	Contractor	Not Applicable
		• Any stockpile should be sited away from existing watercourses and suitably covered to prevent wind erosion and impacts on air and water quality.	Contractor	Not Applicable
7.6.15 to 7.6.17		• Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows. Containers used for the storage of chemical wastes should:		
		• be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;	Contractor	Implemented
		• have a capacity of less than 450L unless the specifications have been approved by the EPD; and	Contractor	Implemented
		• display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation (Cap. 354C).	Contractor	Implemented
		The storage area for chemical wastes should:		
		• be clearly labelled and used solely for the storage of chemical waste;	Contractor	Implemented
		• be enclosed on at least 3 sides;	Contractor	Partially Implemented
		• have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;	Contractor	Implemented
		• have adequate ventilation;	Contractor	Implemented
		• be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and	Contractor	Partially Implemented
		• be arranged so that incompatible materials are adequately separated.	Contractor	Implemented
		The Contractor shall register with EPD as a Chemical Waste Producer. Waste oils and other chemical wastes as defined in the Waste Disposal (Chemical Waste) (General) Regulation will require disposal by appropriate means and could require pre-notification to EPD prior to disposal. Appropriate means include disposal:		
		• via a licensed waste collector; and	Contractor	Implemented
• to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers; or	Contractor	Implemented		
• to a reuser of the waste, under approval from EPD.	Contractor	Not Applicable		
7.6.18 to 7.6.20		• General refuse generated on-site should be stored in enclosed bins or compaction units separate from construction and chemical wastes. A reputable waste collector should be employed	Contractor	Partially Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Review Ref	Location	Environmental Protection Measures/	Implementation Agent	Implementation Status in Construction Phase
		by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily or every second day basis to minimize odour, pest and litter impacts. The burning of refuse on construction sites is prohibited by law.		
		• Separate labelled bins should be provided if feasible.	Contractor	Implemented
		• Office waste can be reduced through recycling of paper if volume is large enough to warrant collection. Participation in a local collection scheme should be considered if one is available.	Contractor	Implemented
7.7.1		• All wastes produced during the construction of the Project shall be handled, stored, and disposed of in accordance with good waste management practices and relevant regulations and requirements.	Contractor	Partially Implemented
		• The mitigation measures recommended in the EIA/EIA review report should form a basis of the WMP to be developed by the Contractor in the construction phase of the Project.	Contractor	Implemented
EP 1.5	<i>General Condition</i>			
N.A	During construction within the Project Boundary.	• The Permit Holder shall display conspicuously a copy of this Permit on the Project site(s) at all vehicular site entrance/exits or at a convenient location for public information at all times. The Permit Holder shall ensure that the most updated information about the Permit, including any amended Permit, is displayed at such locations. If the Permit Holder surrenders a part or the whole of the Permit, the notice he sends to the Director shall also be displayed at the same locations as the original Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site(s).	Contractor	Partially Implemented

Implementation status: Implemented / Partially Implemented / Not Implemented / Not Observed / Not Applicable
