Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
ALL SECTIONS OF THE WORKS				
SCHEDULE OF KEYDATES				
KEY-S2-100	Section II Completion	0		26APR07
KEY-S4-200	Section IV Completion	0		30APR07
KEY-S5-300	Section V Completion	0		31MAR07
SECTION II OF THE WORKS				
AT GRADE SLIP ROAD 'A' & ASSOCIATED WORKS				
Road Works				
SS2-GSA010	Misc. Rdworks/Krbs/Barriers/L.Post/Rd Ducts	15	23JAN07*	08FEB07
SS2-GSA020	Permanent Flex. Pavement @ Slip Rd. A	16	09FEB07	10MAR07
SS2-GSA030	Landscaping Works	5	12MAR07	16MAR07
HOLLOW STRUCTURE OF SLIP ROAD 'A'				
Road Works				
SS2-GSA040	In-situ Parapet Construction / Drainage	30	23JAN07*	09MAR07
SS2-GSA050	Road Surfacing	15	12MAR07	28MAR07
SS2-GSA060	Installation of Parapet Railings	15	29MAR07	19APR07
AT GRADE SLIP ROAD 'D' & ASSOCIATED WORKS				
Drainage Works				
SS2-GSD010	Construction of 225 U-channel	5	23JAN07*	27JAN07
SS2-GSD020	Construction of 375 U-channel	5	29JAN07	02FEB07
SS2-GSD030	Exc,Install,Backfill 600mm Drain Pipe	5	03FEB07	08FEB07
AT GRADE SLIP ROAD 'F' & ASSOCIATED WORKS				
Road Works				
SS2-GSF010	Construction of Sub-soil Drain,DP,M/H,Pipe Wrks	20	23JAN07	14FEB07
SS2-GSF020	Backfilling to Road Formation Level	10	27FEB07	09MAR07
SS2-GSF030	Construction of U-channels	3	10MAR07	13MAR07
SS2-GSF040	Road Surfacing	10	16MAR07	27MAR07
Ecological Barrier Walls				
SS2-GSF050	Wall Stem	20	23JAN07*	14FEB07
SS2-GSF060	Wall Post	20	03FEB07	09MAR07
SS2-GSF070	Install Wall Panels	12	10MAR07	23MAR07
DECK OVER SLIP ROAD 'F'				
Road Works				
SS2-OVF010	Insitu Parapet Construction	25	23JAN07*	03MAR07
SS2-OVF020	Road Surfacing	10	05MAR07	15MAR07
Retaining Wall adjacent to Pier F3				
Construction of Retaining Wall				
SS2-OVF030	F3 Retaining Wall	30	23JAN07*	09MAR07
SS2-OVF050	Backfilling	10	10MAR07	21MAR07
WIDENING WORKS TO CASTLE PEAK ROAD				
Road Works				
SS2-CAS010	Remove Exitsting Street Lamp Post	1	09FEB07*	09FEB07

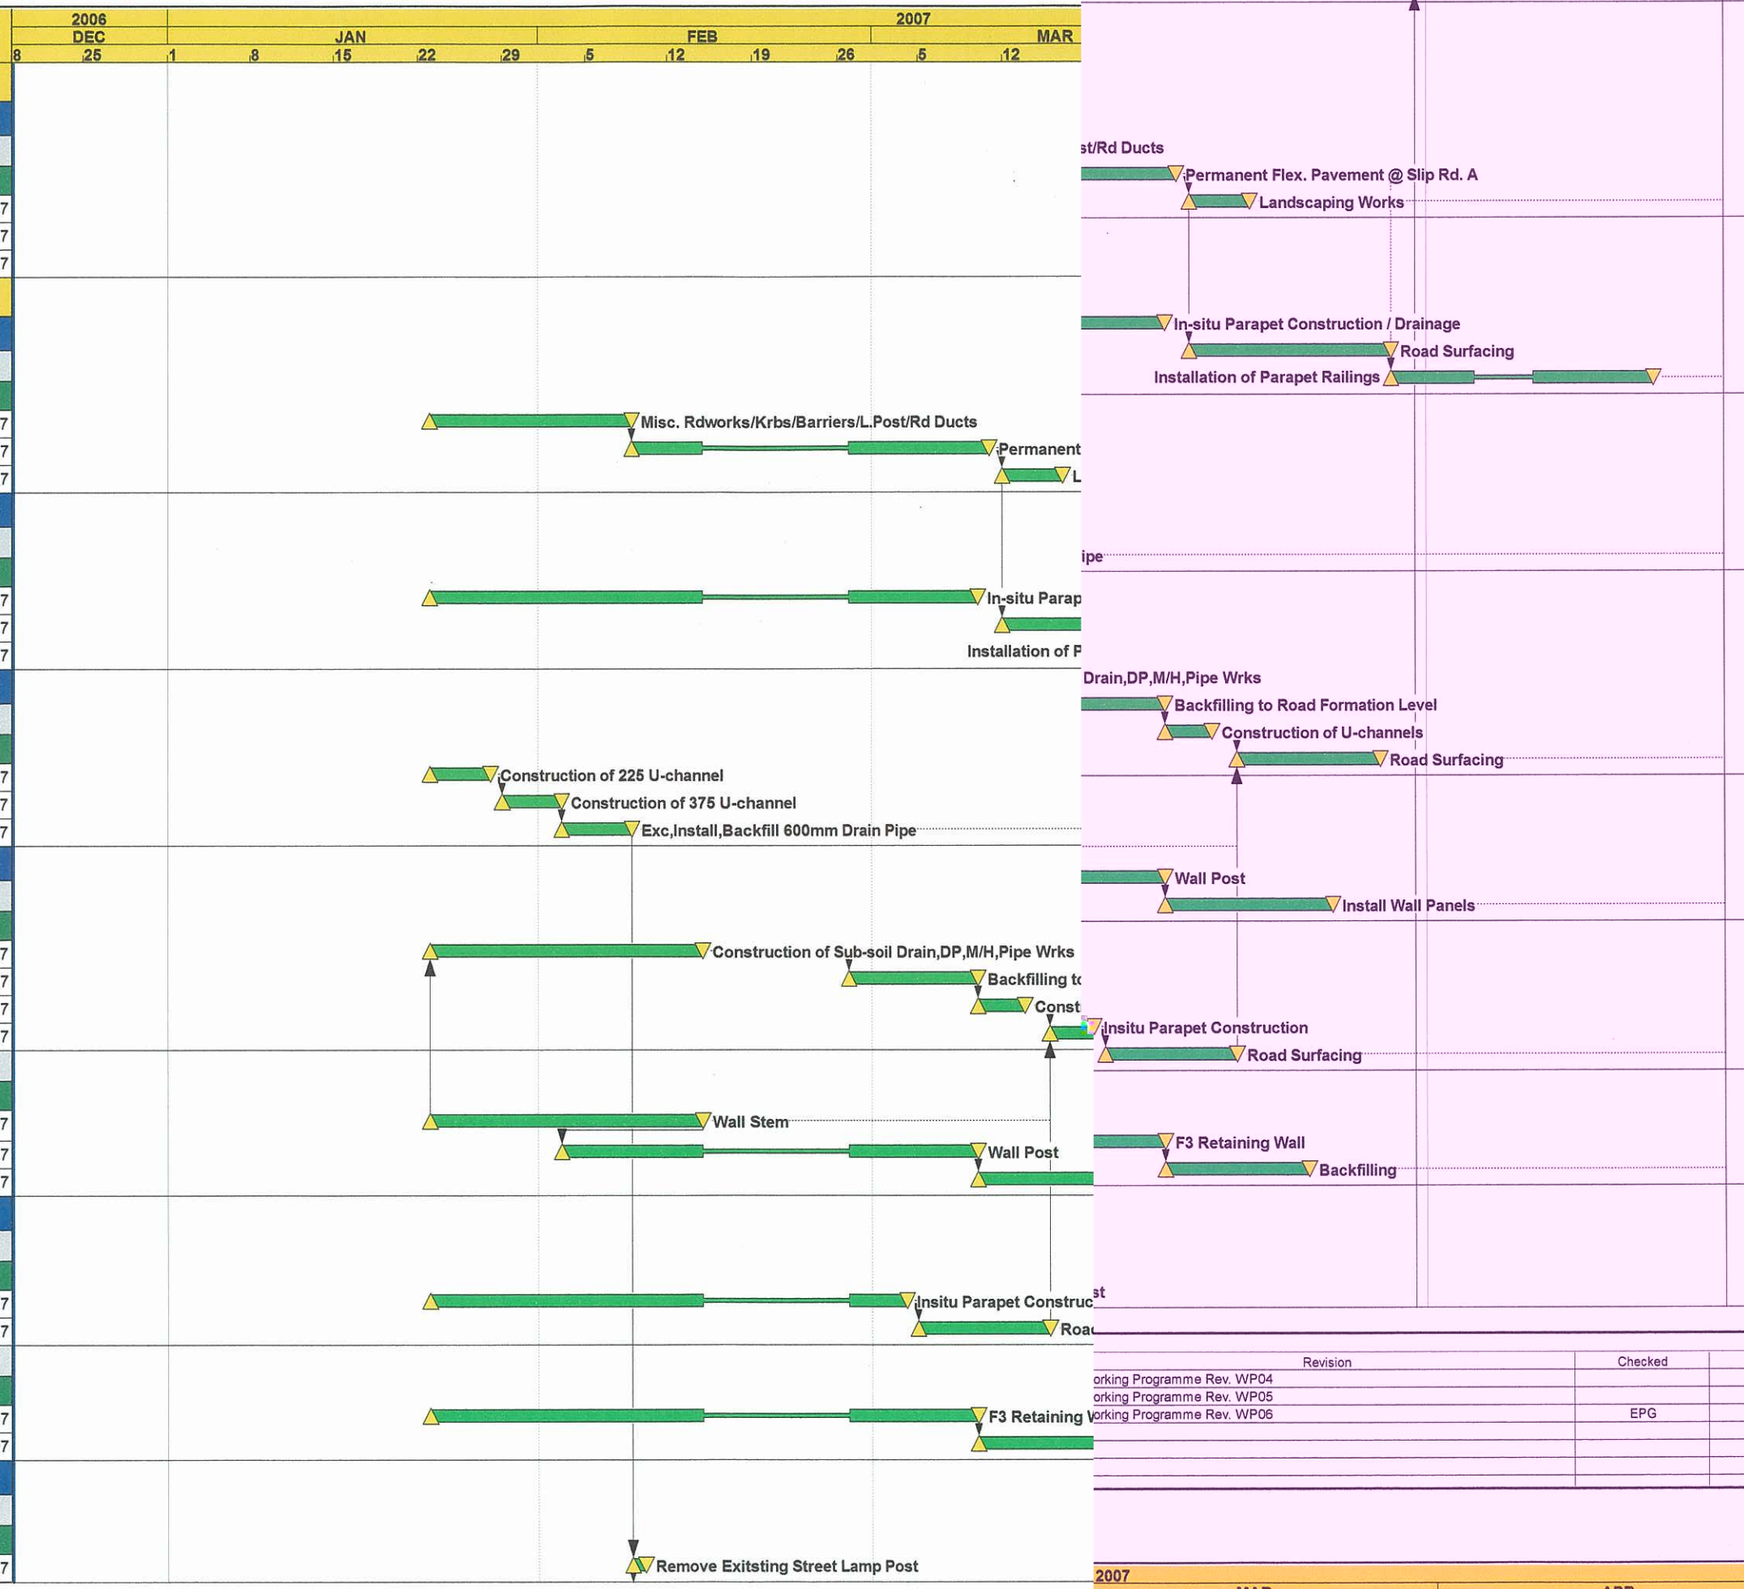

Revision	Checked
orking Programme Rev. WP04	
orking Programme Rev. WP05	
orking Programme Rev. WP06	EPG



Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

© Primavera Systems, Inc.

Early Bar
Progress Bar
Critical Activity

WP06 Sheet 1 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	
26JUN06	Working Programme Rev. WP04
03OCT06	Working Programme Rev. WP05
23JAN07	Working Programme Rev. WP06

Section II Completion
Section IV Comple

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
RESURFACING OF EXISTING NORTHBOUND SAN SHAM RD.				
San Sham Road Zone 2				
TTA Stage 2a				
SS1-S2A010	Implement TTA Stage 2a	1	19JAN07*	19JAN07
SS1-S2A020	Resurfacing 1st Part of Fast Lane (approx. 200m)	5	20JAN07	25JAN07
SS1-S2A030	Demolish 1st Part of Temp. Road	7	26JAN07	02FEB07
SS1-S2A040	Construct Permanent Road (1st Part)	20	03FEB07	09MAR07
TTA Stage 2b				
SS1-S2B010	Implement TTA Stage 2b	1	26JAN07	26JAN07
SS1-S2B020	Resurfacing 2nd Part of Fast Lane (approx. 50m)	7	27JAN07	03FEB07
SS1-S2B030	Road Marking	2	05FEB07	06FEB07
SS1-S2B040	Reinstate Permanent Lamp Post	2	07FEB07	08FEB07
SS1-S2B050	Demolish 2nd Part of Temp Road	3	09FEB07	12FEB07
SS1-S2B060	Construct Permanent Road (2nd Part)	12	13FEB07	09MAR07
SS1-S2B070	Construct Remaining Works	8	10MAR07	19MAR07
SS1-S2B080	Remaining Works at Central Divider	5	14MAR07	19MAR07
Erection of Sign Gantry FVMS1				
SS1-FVM010	Erect Post at Central Divider	2	14MAR07	15MAR07
SS1-FVM020	Erect Post at Merge Area	2	16MAR07	17MAR07
SS1-FVM030	Install FVMS1 Gantry	2	19MAR07	20MAR07
SS1-FVM040	Install Lighting & TCSS	3	21MAR07	23MAR07
SS1-FVM050	T&C TCSS	3	24MAR07	27MAR07
SS1-FVM060	Install Rem Prof Barrier & Ctr Div at Merge Area	2	28MAR07	29MAR07
Remaining Works at the Vehicular Holding Area				
SS1-VHA010	Site Inspection at HVA with Permit	2	19JAN07*	20JAN07
SS1-VHA020	Approval Process to Dem. Exist. Chain Link Fence	14	22JAN07	06FEB07
SS1-VHA030	Dismantle Steel Post & Chain Link Fence	5	07FEB07	12FEB07
SS1-VHA040	Reinstate Chain Link Fence	7	13FEB07	03MAR07
SS1-VHA050	Breaking Existing Road	5	05MAR07	09MAR07
SS1-VHA060	Reconstruct Flexible Pavement	15	10MAR07	27MAR07
SS1-VHA070	Road Marking	3	28MAR07	30MAR07
Opening of San Sham Road (Zone 2)				
SS1-OPN010	Apply Pre-openning Insp. to RMO (7d adv. Notice)	0	23MAR07	
SS1-OPN020	Pre-opening Insp w/ RMO & Open Rd to Traffic	1	31MAR07	31MAR07
SECTION IV OF THE WORKS				
ELEVATED SLIP ROAD 'A' (WA - Pier A4)				
Pre-Hand-over and Hand-over Inspection				
ESA-INSP01	1st Pre-Hand Over Inspection	0		28FEB07*
ESA-INSP11	2nd Pre-hand Over Inspection	0		31MAR07*
ESA-INSP21	Final Hand Over Inspection	0		30APR07
Key Dates				
ESA-KEY010	Completion of Slip Road A	0		30APR07
Milestone Dates				
ESA-MILS01	Traffic Diversion (Slip Road D200 Open)	0		28DEC06*
ESA-MILS02	Insitu Deck Pier A2-A1 & Pier A1-WA (Stage 2b)	0		22JAN07*
ESA-MILS03	Insitu Deck Pier A1 - WA (Mid-Span) (Stage 2c)	0		27FEB07*
Prestress Bottom Continuity				
ESA-PRES01	West Abutment to Pier A4 (Stage 2c)	3	28FEB07	02MAR07

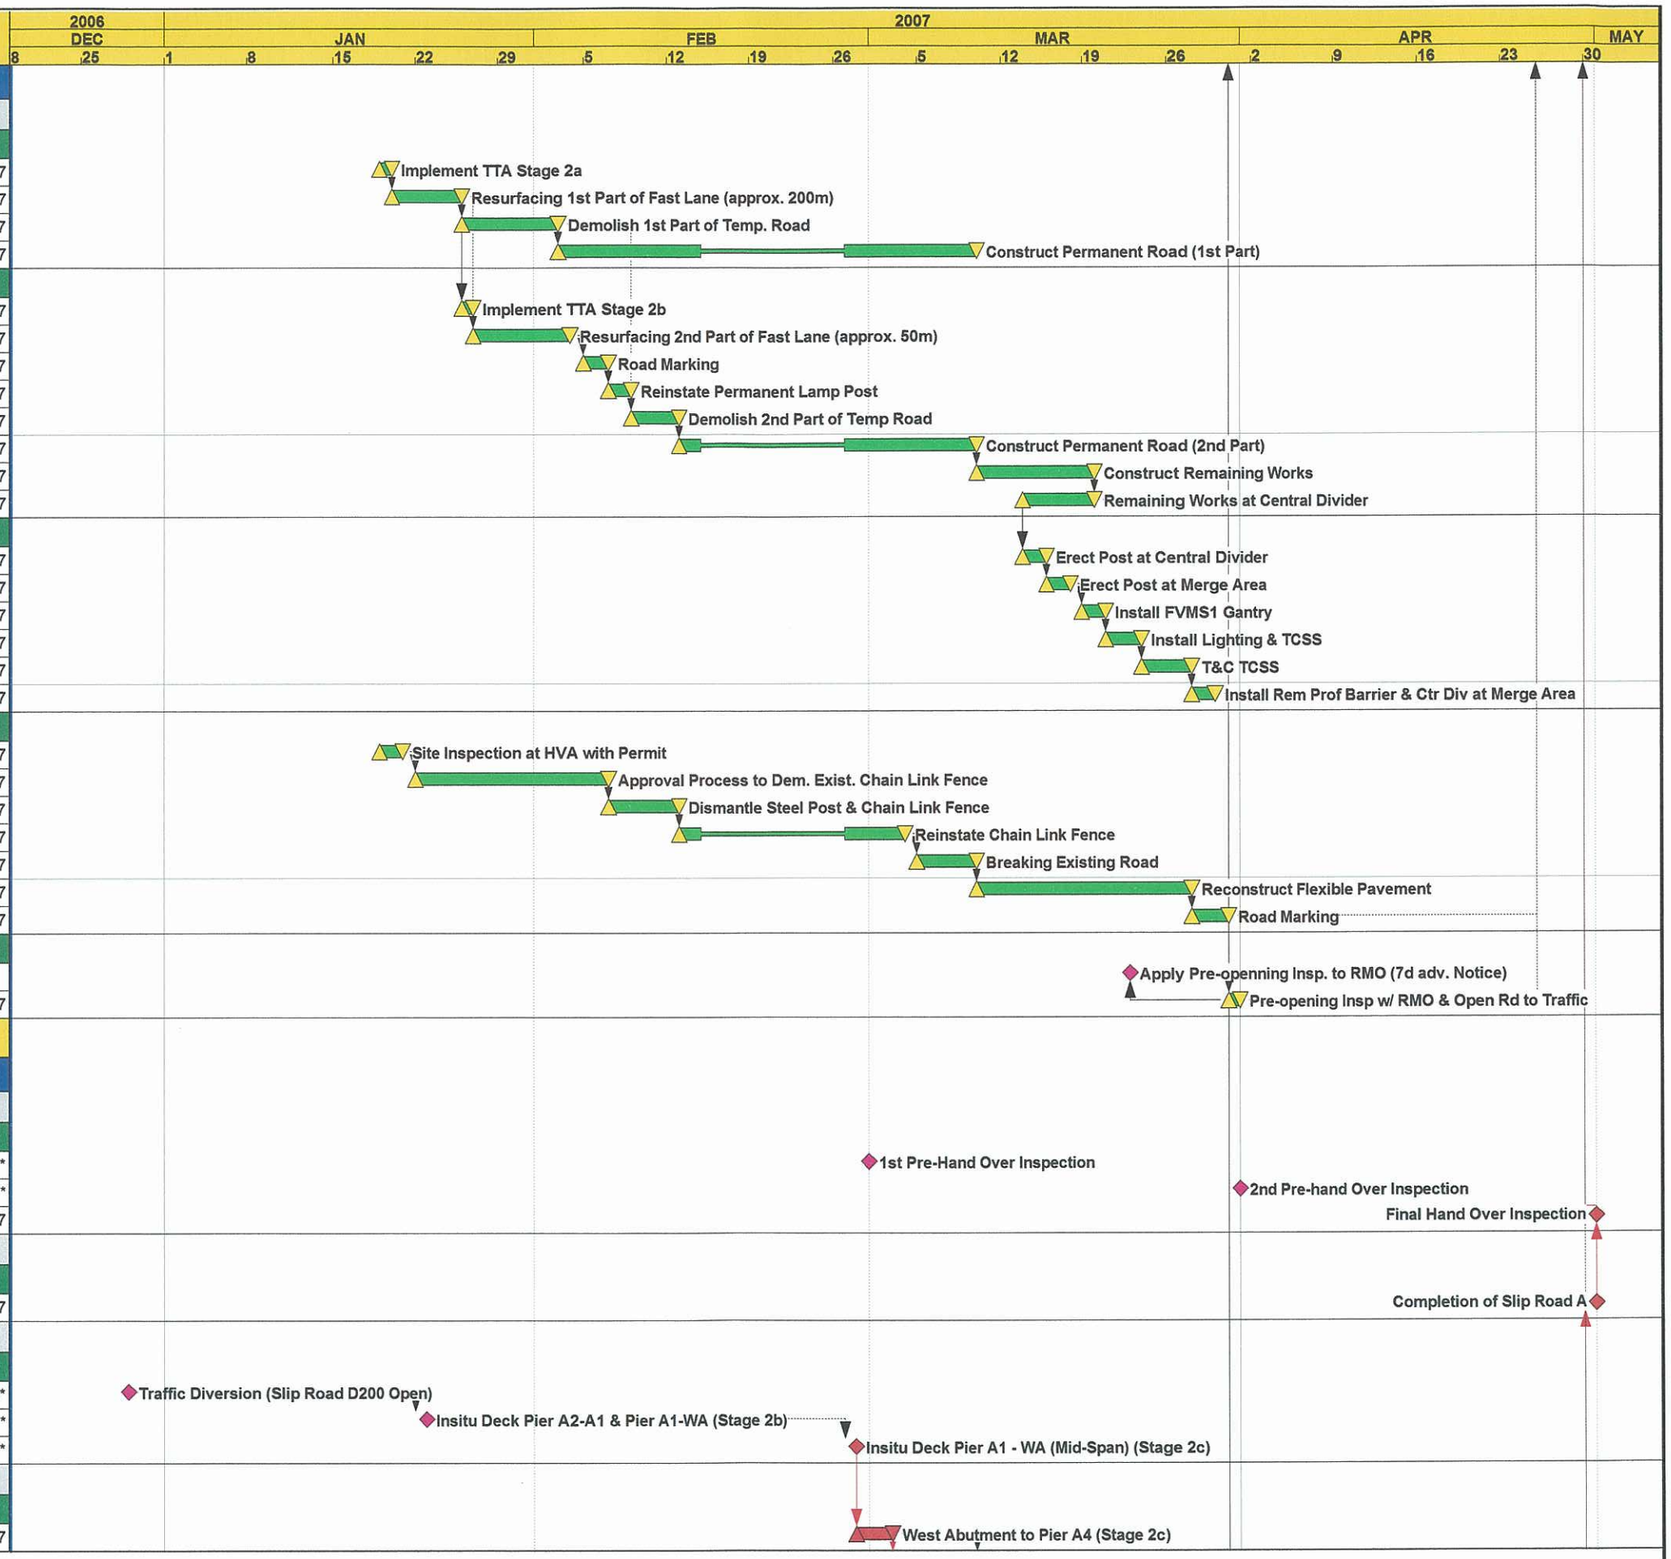

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 3 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
Precast Parapet Installation by Crane/Traveller				
West Abutment - Pier A1 (Span S)				
ESA-PP010	24 units @ 6 units/day	4	03MAR07	07MAR07
Pier A1 - Pier A2 (Span T)				
ESA-PP020	31 units @ 6 units/day	6	08MAR07	14MAR07
Pier A2 - Pier A3 (Span U)				
ESA-PP030	26 units @ 6 units/day	5	15MAR07	20MAR07
Pier A3 - Pier A4 (Span V)				
ESA-PP040	21 units @ 6 units/day	4	21MAR07	24MAR07
Concreting to Parapet Backing				
West Abutment - Pier A1 (Span S)				
ESA-IP010	14 Panels between MJ	6	10MAR07	16MAR07
Pier A1 - Pier A2 (Span T)				
ESA-IP020	16 Panels between MJ	6	17MAR07	23MAR07
Pier A2 - Pier A3 (Span U)				
ESA-IP030	17 Panels between MJ	6	24MAR07	30MAR07
Pier A3 - Pier A4 (Span V)				
ESA-IP100	14 Panels between MJ	6	31MAR07	11APR07
Bridge Deck Drainage System				
ESA-DRN010	Installation of Gully Cover Frame & Weirs	3	12APR07	14APR07
ESA-DRN020	Installation of Carrier Drain Pipes Inside Deck	15	03MAR07	20MAR07
Surfacing to Bridge Deck				
ESA-SUR020	Laying Tack Coat, 1st Layer incl Coring & Test	8	12APR07	20APR07
ESA-SUR030	Laying Final Layer incl Coring & Test	8	17APR07	25APR07
Road Marking				
ESA-MRK010	Road Marking (Slip Road A)	5	24APR07	28APR07
Parapet Railing Installation				
West Abutment to Pier 1A (CH 0+000.00-0+033.00)				
ESA-RL010	Railing Post Installation	3	17MAR07	20MAR07
ESA-RL020	Railing Installation	4	21MAR07	24MAR07
Pier A1 - Pier A2 (CH 0+033.00 - 0+077.70)				
ESA-RL030	Railing Post Installation	3	24MAR07	27MAR07
ESA-RL040	Railing Installation	4	28MAR07	31MAR07
Pier A2 - Pier A3 (CH 0+077.70 - 0+118.40)				
ESA-RL050	Railing Post Installation	3	31MAR07	03APR07
ESA-RL060	Railing Installation	4	04APR07	12APR07
Pier A3 - Pier A4 (CH 0+118.40 - 0+151.40)				
ESA-RL070	Railing Post Installation	3	12APR07	14APR07
ESA-RL080	Railing Installation	4	16APR07	19APR07
Miscellanous Road Works				
ESA-MSC010	Installation of Gully Grating	3	26APR07	28APR07
ESA-MSC020	Repair Core Holes on Road Surfacing	3	26APR07	28APR07
ESA-MSC030	Tidy-Up Area for Hand Over Inspection	3	27APR07	30APR07
Installation of Lighting Poles by Others				
ESA-POL010	Installation of Lighting Poles & Cabling by Othr	0	15MAR07*	
ESA-POL020	Energized Street Lighting	0		30APR07

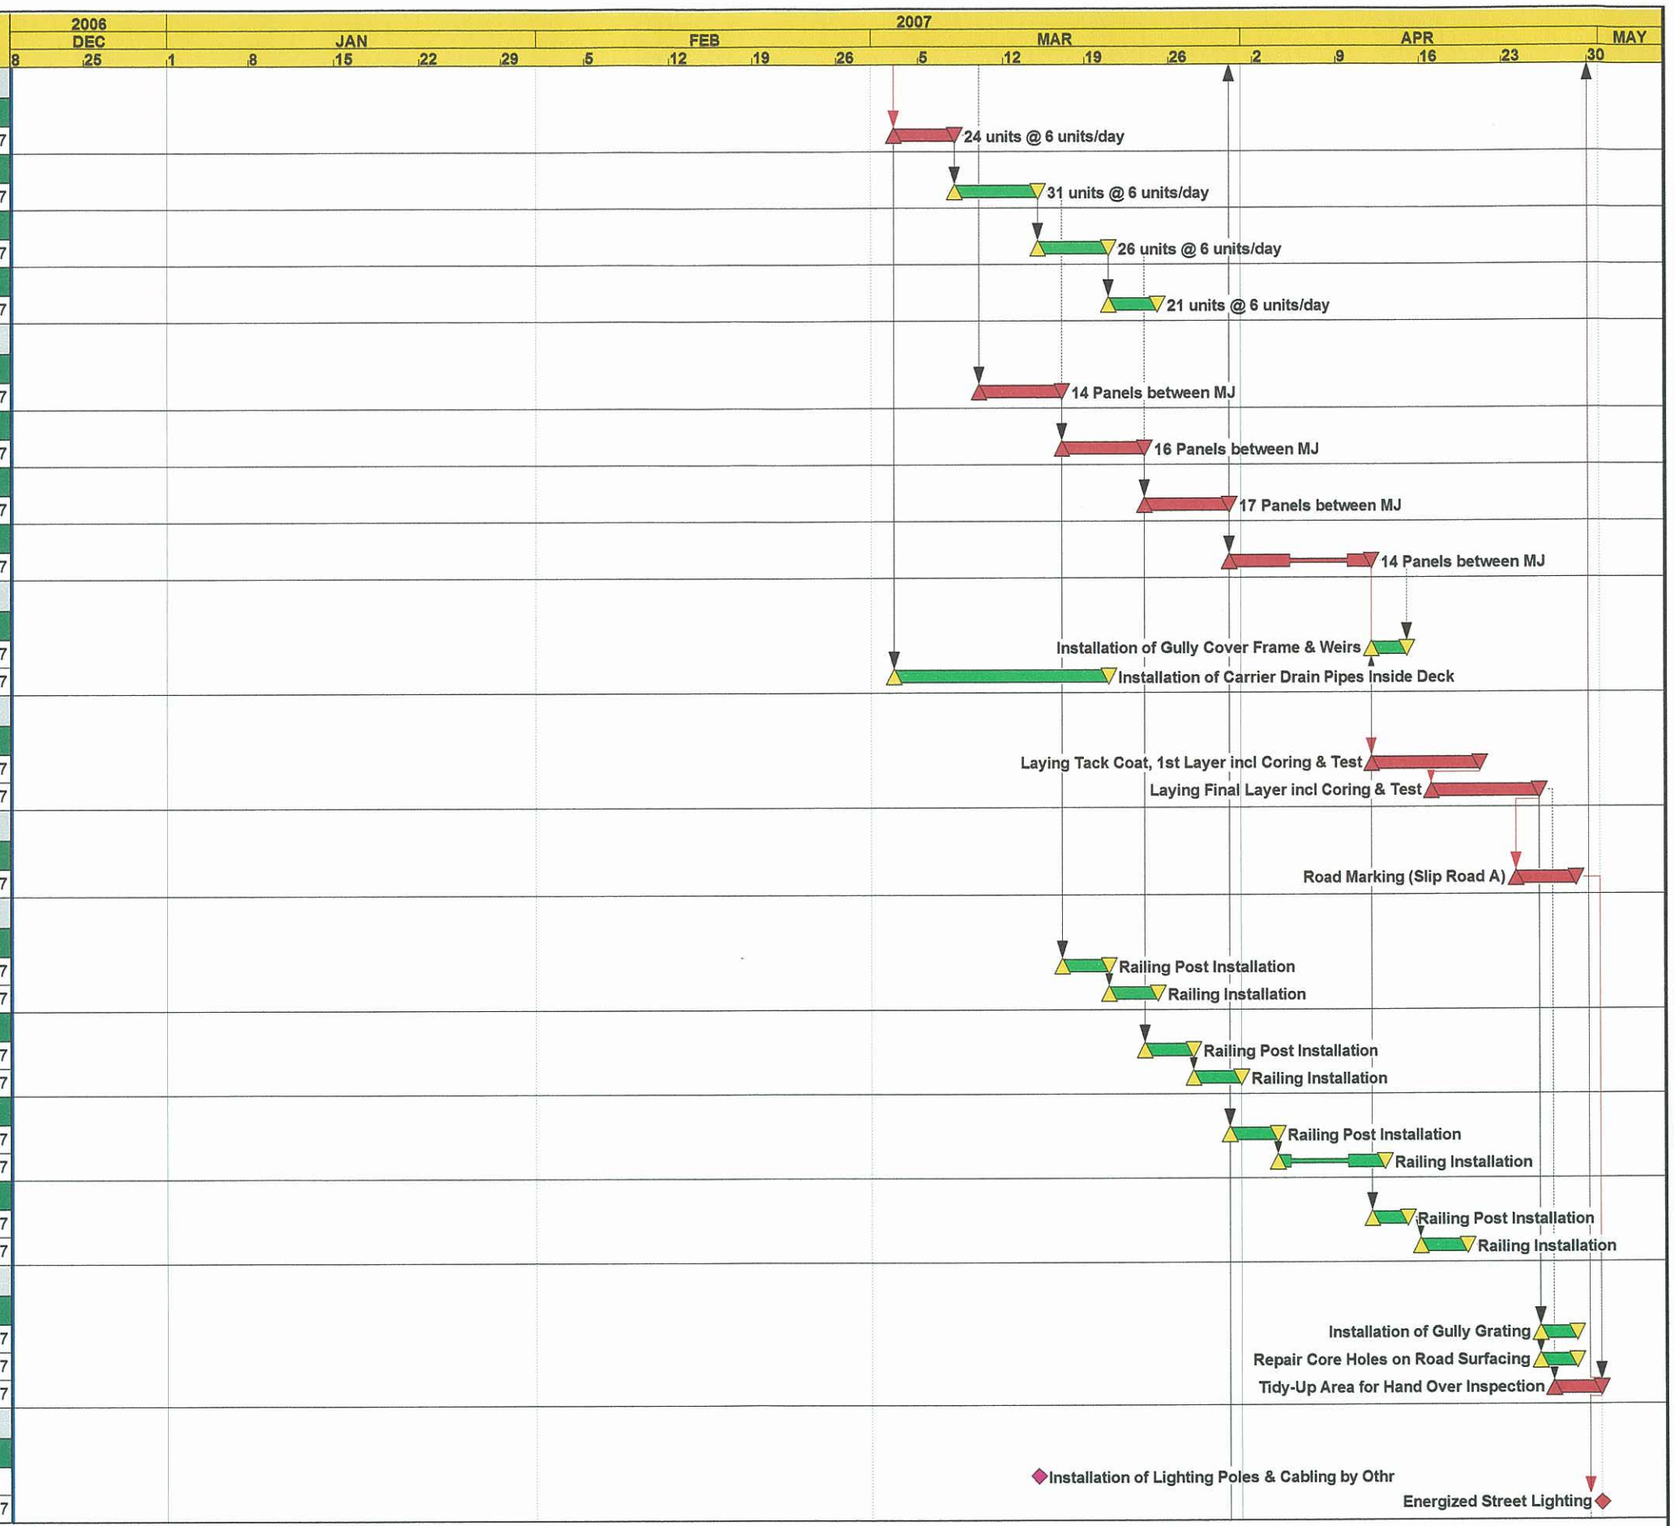

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 4 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
ELEVATED SLIP ROAD 'F' (NA - Pier F1A/F1B)				
Pre-Hand-over and Hand-over Inspection				
ESF-INSP01	1st Pre-Hand Over Inspection	0		28FEB07*
ESF-INSP02	2nd Pre-hand Over Inspection	0		31MAR07*
ESF-INSP03	Final Hand Over Inspection	0		31MAR07
Key Dates				
ESF-KEY010	Completion of Slip Road F	0		31MAR07
Milestone Dates				
ESF-MILS10	Seg Erection Pier F3-F2(13Nos), Stitch,Stressing	0		27FEB07*
Longitudinal Stitch Joints				
ESF-STI010	L1 Joint (North Abutment - Pier F3)	13	19DEC06*	05JAN07
ESF-STI020	L2 Joint (Pier F3 - Pier F2)	10	28FEB07	10MAR07
ESF-STI030	L3 Joint (Pier F2 - branch corner of F1A&B)	12	06JAN07	19JAN07
Prestress Bottom Continuity				
ESF-PRES01	North Abutment - Pier F1B & F1A	3	12MAR07	14MAR07
Precast Parapet Installation by Crane/Traveller				
North Abutment - Pier F3 (Span R)				
ESF-PP010	40 units @ 10pcs/day	4	20JAN07	24JAN07
Pier F3 - Pier F2 (Span Q)				
ESF-PP020	44 units @ 20units/day	3	15MAR07	17MAR07
Pier F2 - Pier F1A & Pier F1B (Span P)				
ESF-PP030	32 units @ 10 units/day	4	25JAN07	29JAN07
Concreting to Parapet Backing				
North Abutment - Pier F3 (Span R)				
ESF-IP010	20 panels of 6m each	6	28FEB07	06MAR07
Pier F3 - Pier F2 (Span Q)				
ESF-IP020	22 Panels of 6m each	6	19MAR07	24MAR07
Pier F2 - Pier F1A & Pier F1B (Span P)				
ESF-IP030	16 Panels of 6m each	6	07MAR07	13MAR07
Waterproofing to Joints				
ESF-WP010	North Abutment - Pier F3	5	07MAR07	12MAR07
ESF-WP020	Pier F3 - Pier F2	3	21MAR07	23MAR07
ESF-WP030	Pier F2 - Pier F1	5	14MAR07	19MAR07
Bridge Deck Drainage System				
ESF-DRN010	Install Gully Cover & Frame NA-F3	2	13MAR07	14MAR07
ESF-DRN020	Install Gully Cover & Frame F3-F2	2	23MAR07	24MAR07
ESF-DRN030	Install Gully Cover & Frame F2-F1	2	14MAR07	15MAR07
ESF-DRN040	Installation of Carier Drain Pipes (Inside Deck)	15	28FEB07	16MAR07
Surfacing to Bridge Deck				
ESF-SUR020	Lay Tack Coat & 1st Layer incl Coring & Test	7	20MAR07	27MAR07
ESF-SUR030	Lay Final Layer incl Coring & Test	8	22MAR07	30MAR07
Road Marking				
ESF-MK010	Road Marking	5	27MAR07	31MAR07

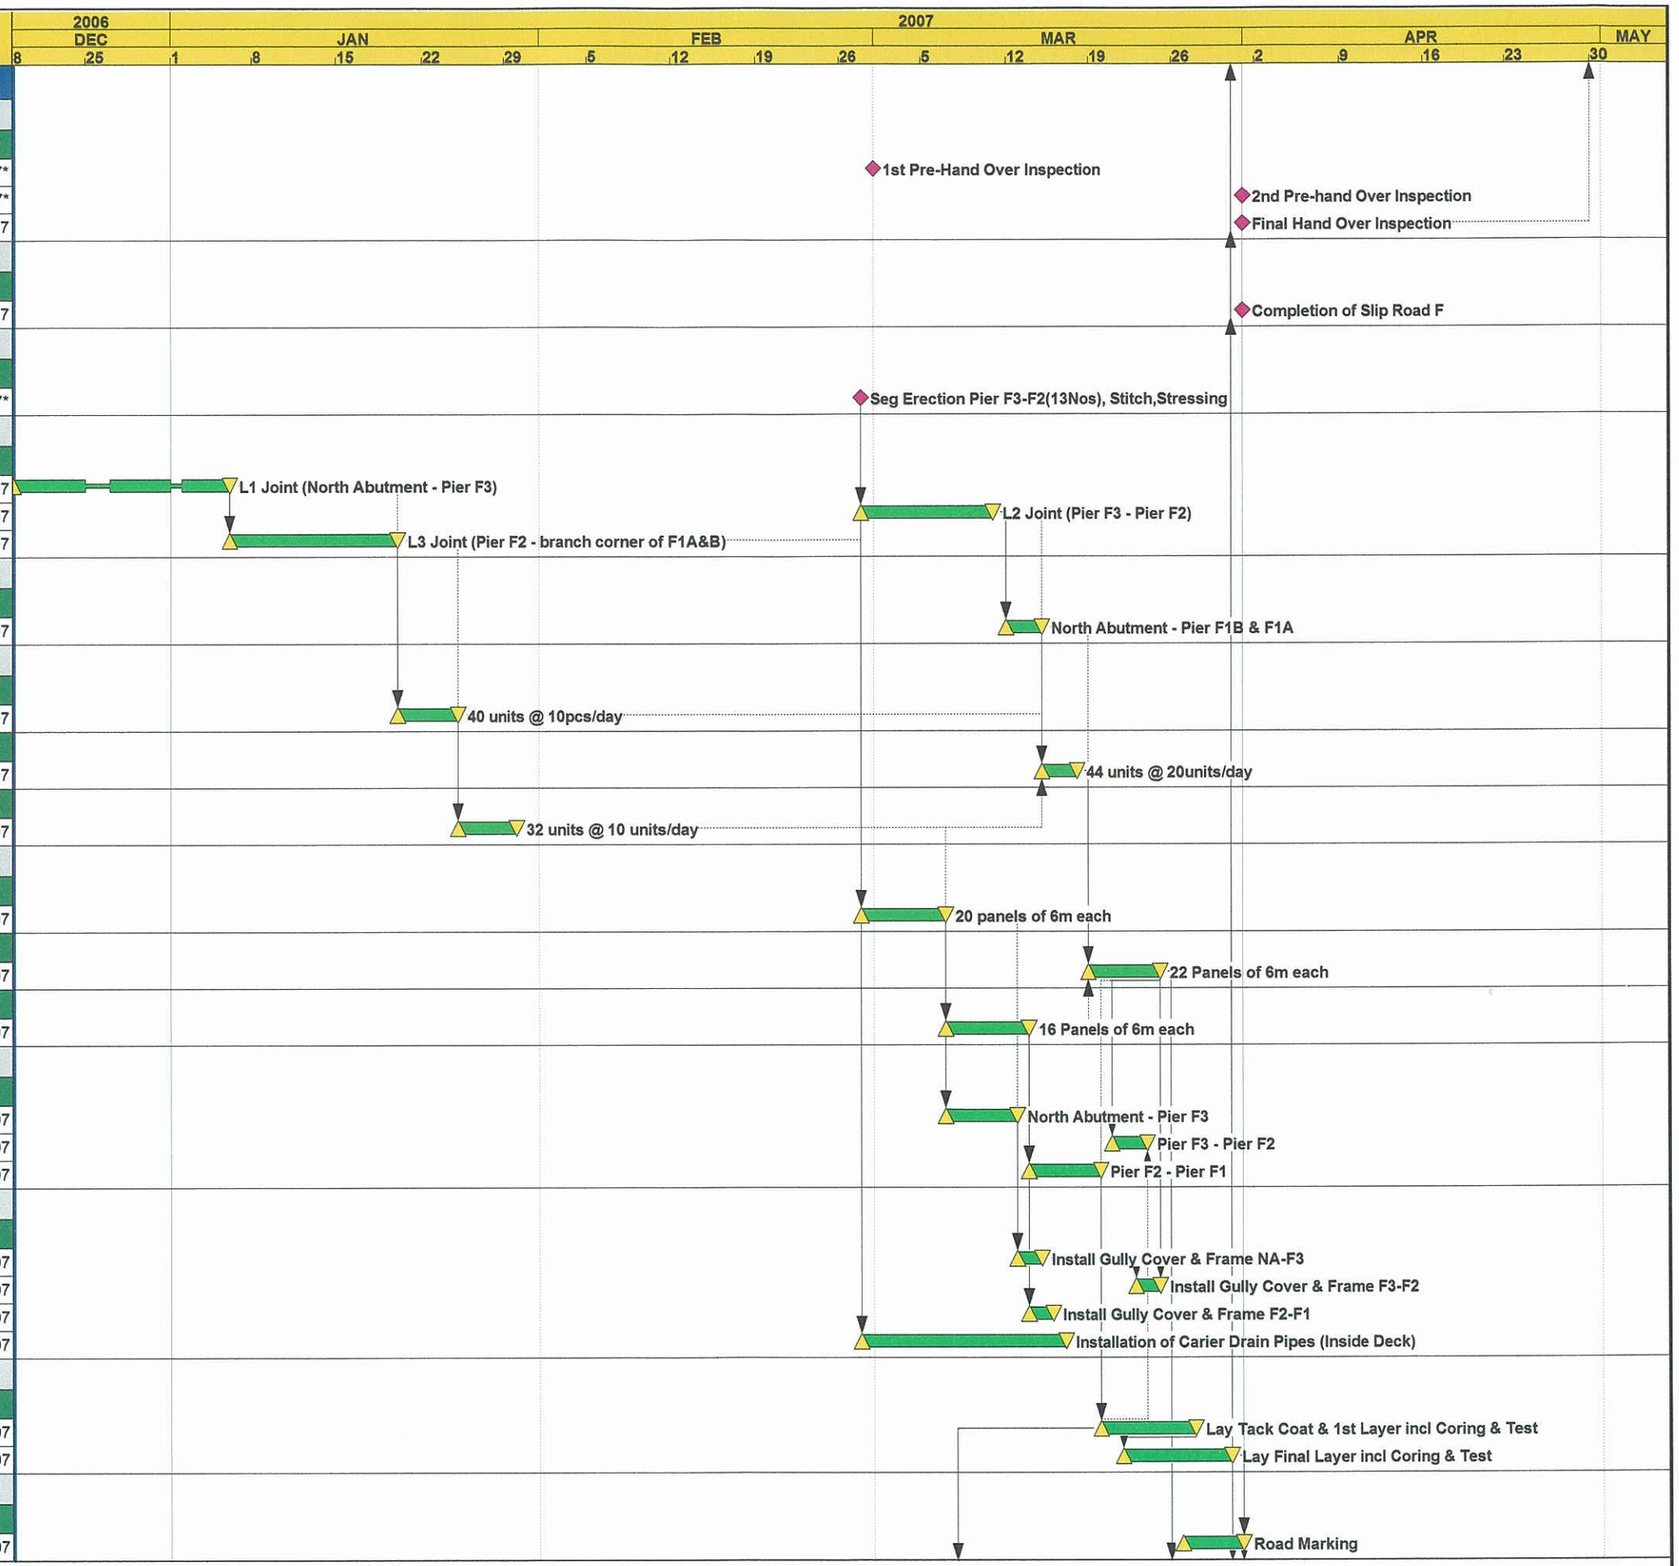

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 5 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
Parapet Railing Installation				
North Abutment to Pier F3 Both Sides (55.193m)				
ESF-RL010	Railing Post Installation	3	08MAR07	10MAR07
ESF-RL020	Railing Installation	4	09MAR07	13MAR07
Pier F3 to Pier F2 Both Sides (61.663m)				
ESF-RL030	Railing Post Installation	3	26MAR07	28MAR07
ESF-RL040	Railing Installation	3	29MAR07	31MAR07
Pier F2 to Pier F1A & F1B Both Sides (48.026m)				
ESF-RL050	Railing Post Installation	3	12MAR07	14MAR07
ESF-RL060	Railing Installation	4	15MAR07	19MAR07
Miscellanous Road Works				
ESF-MSC010	Installation of Gully Grating	4	27MAR07	30MAR07
ESF-MSC020	Repair Core Holes on Flexible Pavement	4	28MAR07	31MAR07
ESF-MSC030	Tidy-Up Area for Handover Final Inspection	5	27MAR07	31MAR07
Installation of Lighting Poles by Others				
ESF-POL010	Installation of Lighting Poles by Others	0	15MAR07*	
ESF-POL020	Energized Street Lighting	0		31MAR07
SECTION V OF THE WORKS				
AT GRADE SLIP ROAD 'C'				
Drainage Works				
SS5-GSC010	Construct U-Channel (Hollow Section - S.Rd.C)	10	05FEB07	27FEB07
SS5-GSC020	Lay & Backfill 375d Pipe (CP14-Existing Nullah)	4	05FEB07	08FEB07
SS5-GSC030	Construct Head Wall No.2 (Inlet)	6	09FEB07	27FEB07
SS5-GSC040	Irrigation Works	12	14FEB07	10MAR07
Road Works				
SS5-GSC060	Watermain 150dia. Pipe Connection	7	23JAN07*	30JAN07
SS5-GSC070	Cable Drawpit & Crossroad Ducts	4	31JAN07	03FEB07
SS5-GSC080	Road Works (Kerbs,Sub-Base,Flexible Pavement)	15	12MAR07	28MAR07
SS5-GSC090	Construction of Footpath (Formation,Paving Bloc)	8	22MAR07	30MAR07
Site Formation, Landscape, GTech Instr.				
SS5-GSC100	Site Formation (M1 - M9)	30	23JAN07*	09MAR07
SS5-GSC120	Slope Wks & Gtech. Instrumentation	23	06FEB07	15MAR07
SS5-GSC130	Landscaping & Planting	26	01MAR07	30MAR07
ELEVATED SLIP ROAD 'B' (EA - Pier B15)				
Pre-Hand-over and Hand-over Inspection				
ESB-INSP01	1st Pre-Hand Over Inspection	0		10JAN07*
ESB-INSP02	2nd Pre-hand Over Inspection	0		01MAR07*
ESB-INSP03	Final Hand Over Inspection	1	31MAR07	31MAR07
Key Dates				
ESB-MILS11	Completion of Slip Road B	0		31MAR07
Milestone Dates				
ESB-MILS01	Concrete Stitch between Pier B9 - Pier B10	0		26JAN07*
ESB-MILS02	Prestressing East Abutment to Pier B6	0		20DEC06*
ESB-MILS03	Prestressing Pier B6 - Pier B8	0		21DEC06*
ESB-MILS04	Prestressing Pier B8 - Pier B11	0		31JAN07*

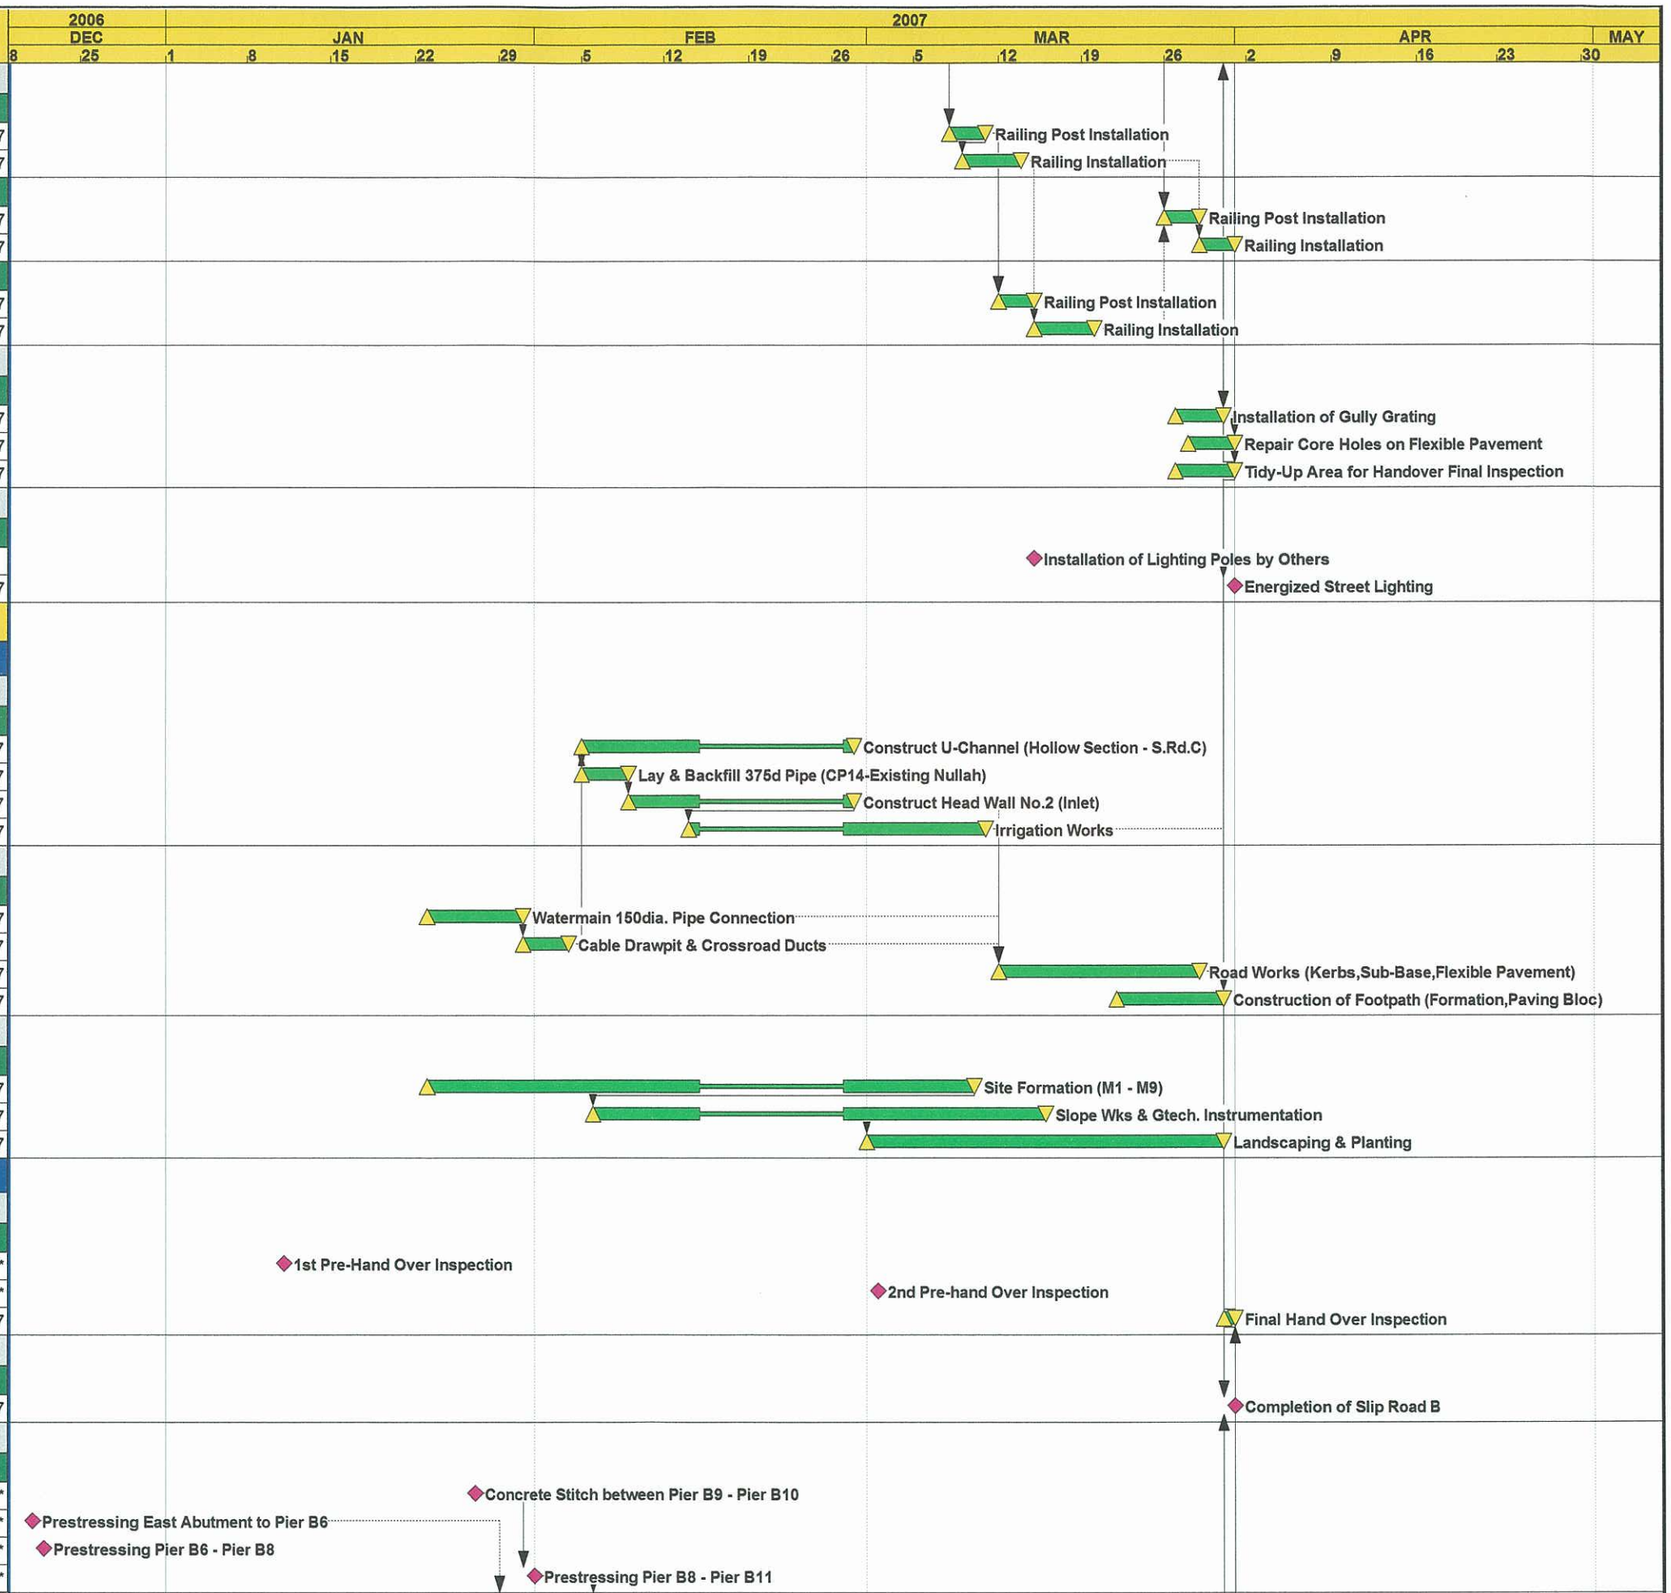

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 6 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
ESB-MILS05	Prestressing Pier B11 - Pier B13	0		22DEC06*
ESB-MILS06	Prestressing Pier B13 to Pier B15	0		20DEC06*
Precast Parapet Installation by Crane/Traveller				
ESB-PP010	EA toward Pier B15 (140unt@20/day) as of 16/1/07	7	29JAN07	05FEB07
Concreting to Parapet Backing				
East Abutment to Pier B1 (Span A)				
ESB-IP0101	3 Panels (as of 16/1/07)	6	06FEB07	12FEB07
Pier B1 - Pier B2 (Span B)				
ESB-IP0102	1 Panel (as of 16/1/07)	6	06FEB07	12FEB07
Pier B2 -Pier B3 (Span C)				
ESB-IP0103	3 Panels (as of 16/1/07)	6	06FEB07	12FEB07
Pier B3 - Pier B4 (Span D)				
ESB-IP0104	4 Panels (as of 16/1/07)	6	06FEB07	12FEB07
Pier B4 - Pier B5 (Span E)				
ESB-IP0105	8 Panels (as of 16/1/07)	6	06FEB07	12FEB07
Pier B5 - Pier B6 (Span F)				
ESB-IP0106	8 Panels (as of 16/1/07)	6	06FEB07	12FEB07
Pier B6 - Pier B7 (Span G)				
ESB-IP0107	20 Panels (as of 16/1/07)	6	17MAR07	23MAR07
Pier B7 - Pier B8 (Span H)				
ESB-IP0108	18 Panels (as of 16/1/07)	6	17MAR07	23MAR07
Pier B8 - Pier B9 (Span I)				
ESB-IP0109	16 Panels (as of 16/1/07)	6	10MAR07	16MAR07
Pier B9 - Pier B10 (Span J)				
ESB-IP0110	20 Panels (as of 16/1/07)	6	10MAR07	16MAR07
Pier B10 - Pier B11 (Span K)				
ESB-IP0112	22 Panels (as of 16/1/07)	6	03MAR07	09MAR07
Pier B11 - Pier B12 (Span L)				
ESB-IP0113	18 Panels (as of 16/1/07)	6	03MAR07	09MAR07
Pier B12 - Pier B13 (Span M)				
ESB-IP0114	16 Panels (as of 16/1/07)	6	13FEB07	02MAR07
Pier B13 - Pier B14 (Span N)				
ESB-IP0115	14 Panels (as of 16/1/07)	6	13FEB07	02MAR07
Pier B14 - Pier B15 (Span O)				
ESB-IP0116	10 Panels (as of 16/7/07)	6	06FEB07	12FEB07
Installation of Movement Joints				
ESB-MJ010	@ East Abutment	3	13FEB07	27FEB07
ESB-MJ020	@ Pier B5	3	28FEB07	02MAR07
ESB-MJ030	@ Pier B9	3	17MAR07	20MAR07
Waterproofing to Joints				
1st Stage				
ESB-WP010	Surface Preparation and apply 1st Coat	7	06FEB07	13FEB07
ESB-WP020	Apply 2nd Coat	7	12FEB07	02MAR07
2nd Stage				
ESB-WP030	Surface Preparation and apply 1st Coat	7	13MAR07	20MAR07
ESB-WP040	Apply 2nd Coat	7	17MAR07	24MAR07
Bridge Deck Drainage System				
1st Stage				
ESB-DRN010	Setting Out Level of Gully Cover	5	13FEB07	01MAR07
ESB-DRN020	Installation of Gully Cover Frame and Weir	5	02MAR07	07MAR07
ESB-DRN030	Installation of Carrier Pipes (inside Deck)	20	06FEB07	12MAR07

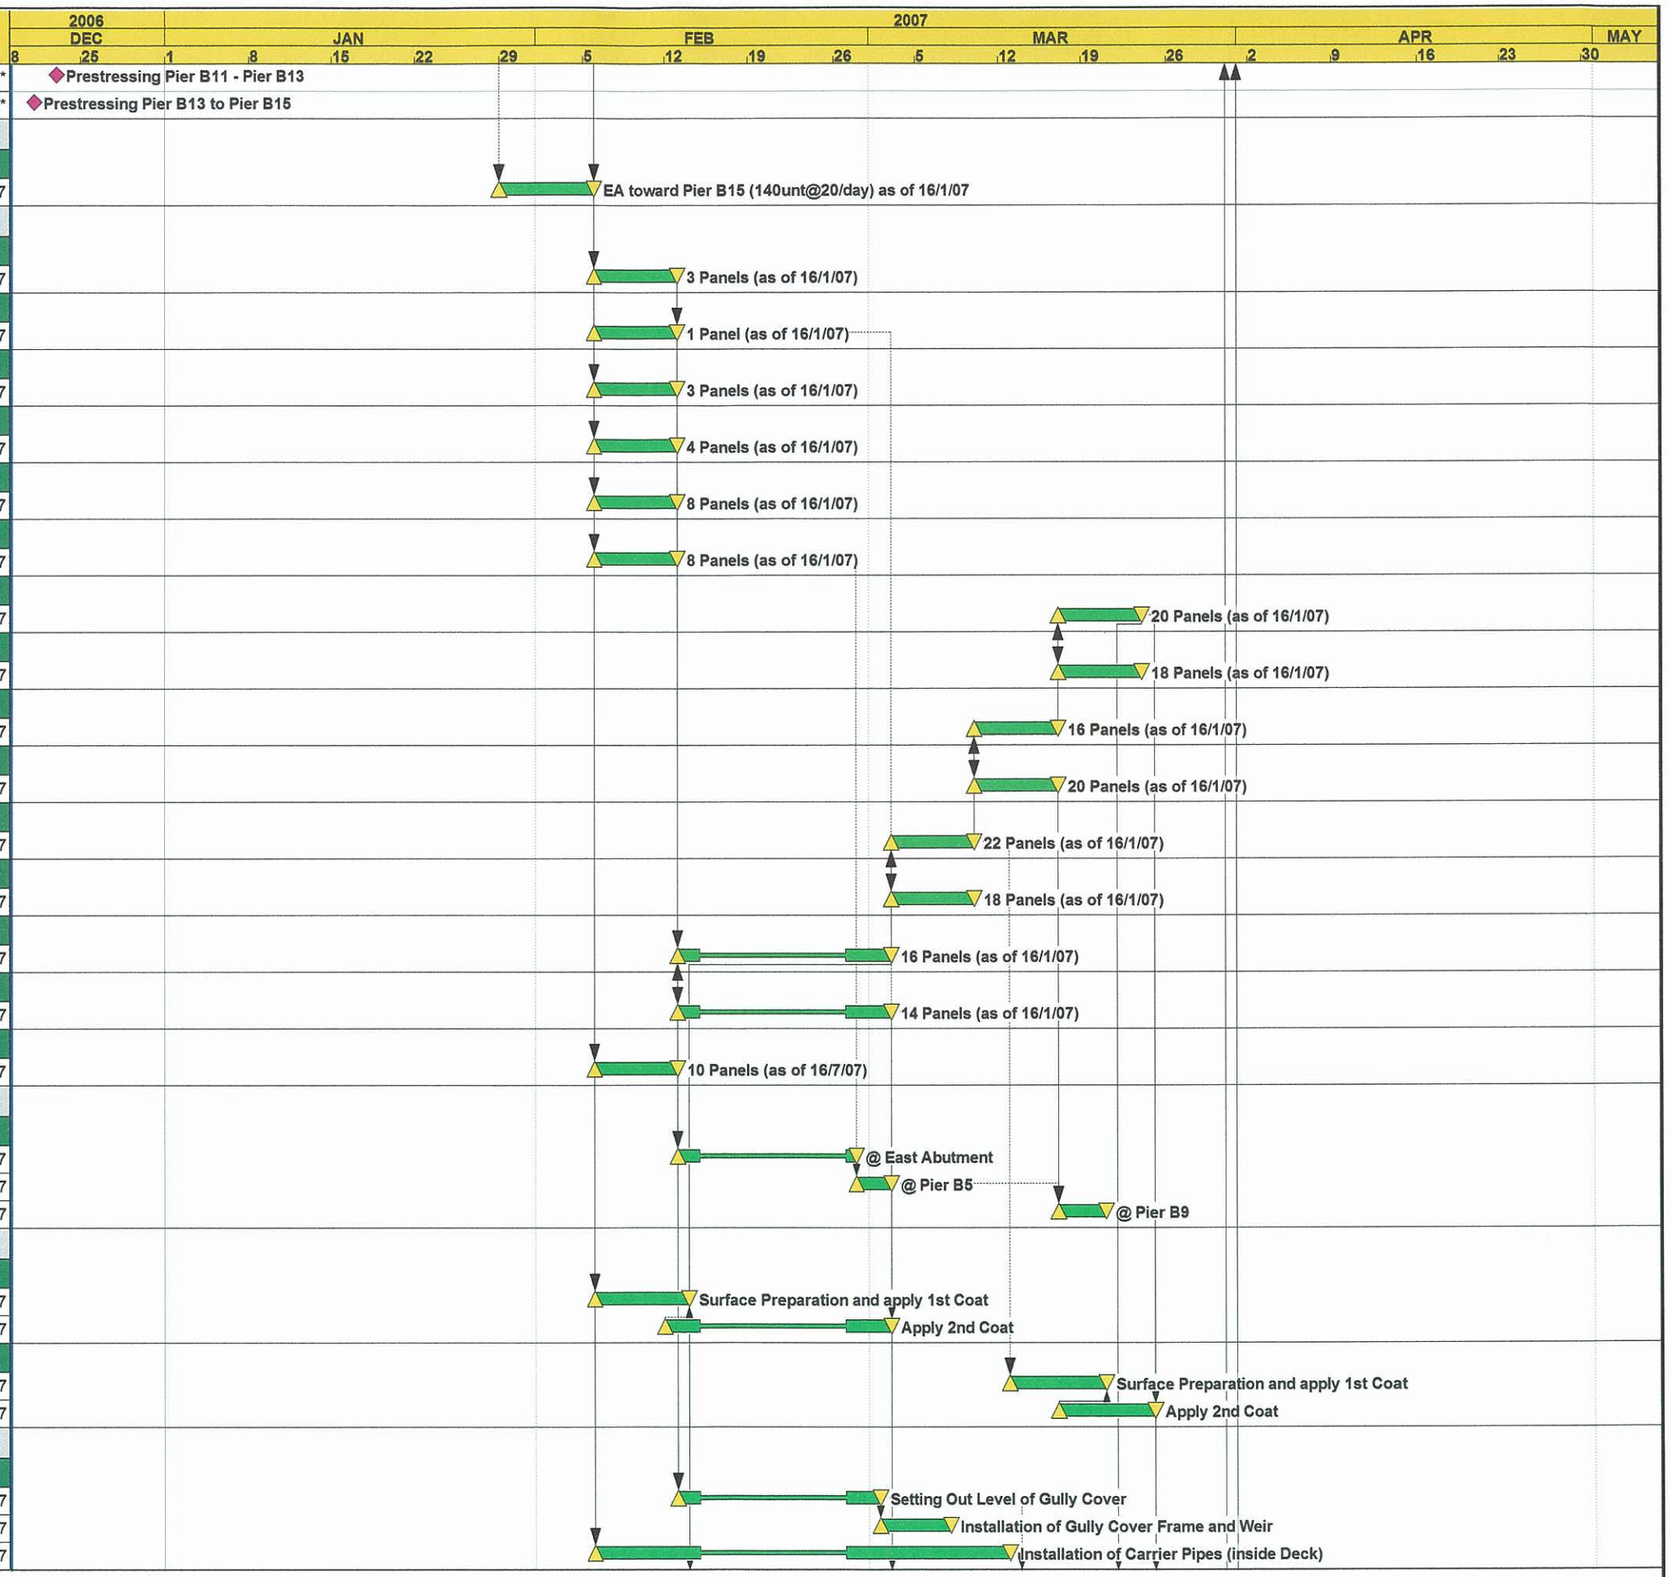

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 7 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
2nd Stage				
ESB-DRN040	Setting Out Level of Gully Cover	5	14MAR07	19MAR07
ESB-DRN050	Installation of Gully Cover Frame and Weir	5	20MAR07	24MAR07
Surfacing to Bridge Deck				
1st Stage				
ESB-SUR010	Set Out Level of 1st Layer & Final Layer	5	14FEB07	02MAR07
ESB-SUR020	Laying Tack Coat, 1st Layer incl Coring & Test	10	03MAR07	14MAR07
ESB-SUR030	Laying 2nd Layer incl Coring & Test	10	09MAR07	20MAR07
2nd Stage				
ESB-SUR040	Set Out Level of 1st Layer & Final Layer	5	16MAR07	21MAR07
ESB-SUR050	Laying Tack Coat, 1st Layer incl Coring & Test	5	22MAR07	27MAR07
ESB-SUR060	Laying 2nd Layer incl Coring & Test	5	24MAR07	29MAR07
Road Marking				
ESB-MRK010	Road Marking	10	21MAR07	31MAR07
Parapet Railing Installation				
ESB-RL010	Railing Installation	25	03MAR07	31MAR07
Miscellanous Road Works				
ESB-MCS010	Installation of Gully Grating	5	26MAR07	30MAR07
ESB-MCS020	Repair Core Holes on Surfacing Materials	5	27MAR07	31MAR07
ESB-MCS030	Tidy - Up Area for Handover Final Inspection	5	27MAR07	31MAR07
Installation of Lighting Poles by Others				
ESB-POL010	Installation of Lighting Poles and Cabling	0	15MAR07*	
ESB-POL020	Energized Street Lighting	0		31MAR07

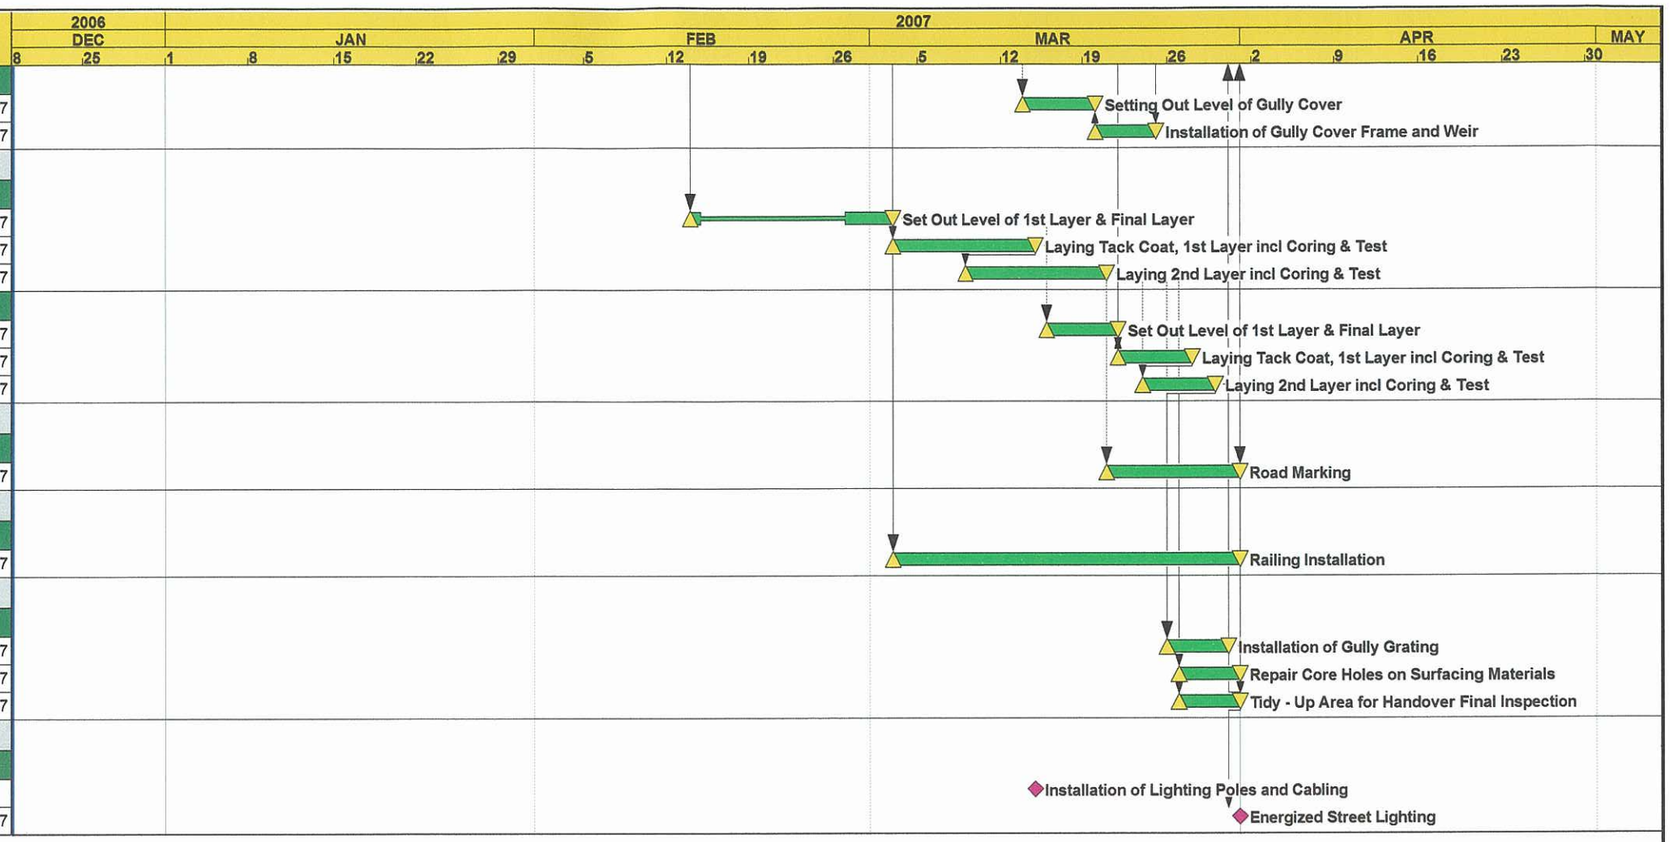

Start Date 19DEC06
Finish Date 30APR07
Data Date 19DEC06

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

WP06 Sheet 8 of 8

CHUN WO CONSTRUCTION & ENGINEERING CO. LTD.
CONTRACT NO. HY/2004/09
IMPROVEMENTS TO SAN TIN INTERCHANGE
Works Programme (WP06)

Date	Revision	Checked	Approved
26JUN06	Working Programme Rev. WP04		J. Yip
03OCT06	Working Programme Rev. WP05		J. Yip
23JAN07	Working Programme Rev. WP06	EPG	J. Yip
