Programme and Progress for the Construction of Jetty at Lung Kwu Chau (CV/2002/11)

General	Activities	Duration	Early Start	Early Finish	Actual Start	Actual Finish
FR_1000	Commencement	0	4 Apr,03	-		
FR_1010	Mobilization / setup	21	4 Apr,03	24 May, 2003	4 Apr,03	24 May, 2003
FR_2000	Boundary monitoring	40	15 Apr,03	24 May, 2003	18 Apr,03	15 May,03
FR_2003	Impact monitoring	219	25 May, 2003	29 Dec,03	9 June,03	24 Sept,03
FR_2007	Post project monitoring	28	30 Dec,03	26 Jan,04		
FR_3100	Notice to Mariners	38	23 Apr,03	22 May, 2003	25 Apr,03	22 May, 2003
FR_3200	Dredging permit	28	25 Apr,03	22 May, 2003	25 Apr,03	22 May, 2003
FR_3000	Site offices - proposal and approval	13	4 Apr,03	24 Apr,03	4 Apr,03	14 Apr,03
FR_3110	Site offices - erection	28	25 Apr,03	22 May, 2003	25 Apr,03	22 May, 2003
FR_4000	Precast units - information & approval	33	29 Apr,03	13 May, 2003	14 June,03	13 June,03
FR_4100	Precast units - fabrication	95	16 May, 2003	29 July, 2003	13 June,03	4 Aug,03
FR_5000	B&M - submission & approval	31	25 Apr,03	29 May, 2003	14 Aug,03	2 Sept,03
FR_5100	E&M - order & delivery	60	30 May, 2003	28 July, 2003	1 Sept,03	
FR_6000	No dredging for approach channel	123	1 May, 2003	31 Aug,03		
FR_9999	Anydate	0	-	29 Dec,03		
Jetty						
Dredging						
JT_1000	Dredging - foundation	13	25 May, 2003	8 June, 2003	11 June,03	27 June,03
JT_1100	Dredging - approach channel	20	1 Sept,03	20 Sept,03	25 Sept,03	26 Sept,03
Rockfill						
JT_2000	G7/1 for Jetty foundation	19	9 June, 2003	18 June, 2003	3 July,03	7 July,03
JT_2200	Tri bars block	17	19 Aug,03	28 Aug,03	30 July,03	6 Aug,03
JT_2300	Cement fill behind jetty coping	8	15 Oct,03	21 Oct,03	11 Sept,03	17 Sept,03
JT_2400	Type 1 sub-base for jetty	5	22 Oct,03	28 Oct,03		
Precast Units						
JT_3000	Setting precast blocks at jetty to level - (6m??	21	19 June, 2003	9 July, 2003	14 July,03	2 Aug,03
JT_3005	Setting precast blocks at jetty to finish level	6	29 Aug,03	3 sept,03	3 Aug,03	5 Aug,03
R.C Works						
JT_4000	Cast Jetty coping & step	40	4 Sept,03	13 Oct,03	31 Aug,03	
JT_5010	Cast Jetty slab	15	27 Oct,03	5 Nov,03	30 July,03	
Rockfill						
JT_2010	G7/1 for pipe foundation	10	10 July, 2003	19 July, 2003	14 Aug,03	15 Aug,03
JT_2020	G7/1 for carwall - landside (13.5m)	18	30 July, 2003	8 Aug,03	27 Aug,03	4 Sept,03
JT_2025	G7/1 for Carwall - seaside (6.5m)	7	4 Sept,03	10 sept,03	27 Aug,03	4 Sept,03
JT_2100	Type 3 cement	20	21 sept,03	10 Oct,03		
JT_2150	Type 1 sub-base for carwall	5	24 Oct,03	28 Oct,03		
Precast Units						
JT_3015	Setting precast blocks of carwall - landside (13m)	10	5 Aug,03	18 Aug,03	18 Sept,03	20 Sept,03
JT_3015	Setting precast blocks of carwall - seaside (9m)	19	11 Sept,03	30 Sept,03	15 Sept,03	29 Sept,03
JT_3030	Setting precast pipes	10	20 July,03	29 July,03	22 Aug,03	23 Aug,03
JT_3050	Setting connecting carwall (Precast)	3	11 Oct,03	13 Oct,03		
R.C Works						
JT_4015	Cast carwall in-situ concrete	17	21 Sept,03	30 Sept,03	5 Aug,03	
JT_4020	Cast carwall coping	19	14 Oct,03	23 Oct,03	28 July,03	20 Sept,03
JT_5020	Cast carwall slab	15	6 Nov,03	20 Nov,03	4 Aug,03	
Trestle						
Excavation						
FT_1000	Excavation for foundation (13 nos)	109	25 May,03	11 Oct,03	25 Sept,03	
R.C Works						
FT_2000	Cast foundation	140	24 June,03	15 Nov,03		
FT_2100	Cast slab	144	24 July,03	14 Dec,03		
Jetty Furniture						
JT_5000	Bollard and Fender	30	6 Nov,03	5 Dec,03		
JT_5050	Handrail and sign	30	17 Nov,03	16 Dec,03		
E&M						
JT_6000	Pillar box and pits	23	29 Oct,03	19 Nov,03		
JT_6100	Lighting - installation	19	21 Nov,03	8 Dec,03		
JT_6150	Lighting - testing & commissioning	6	9 Dec,03	14 Dec,03		
Demolition						
JT_9999	Demolition of old Jetty	13	15 Dec,03	29 Dec,03		

Notes : Programme — Progress — 30 30% works completed

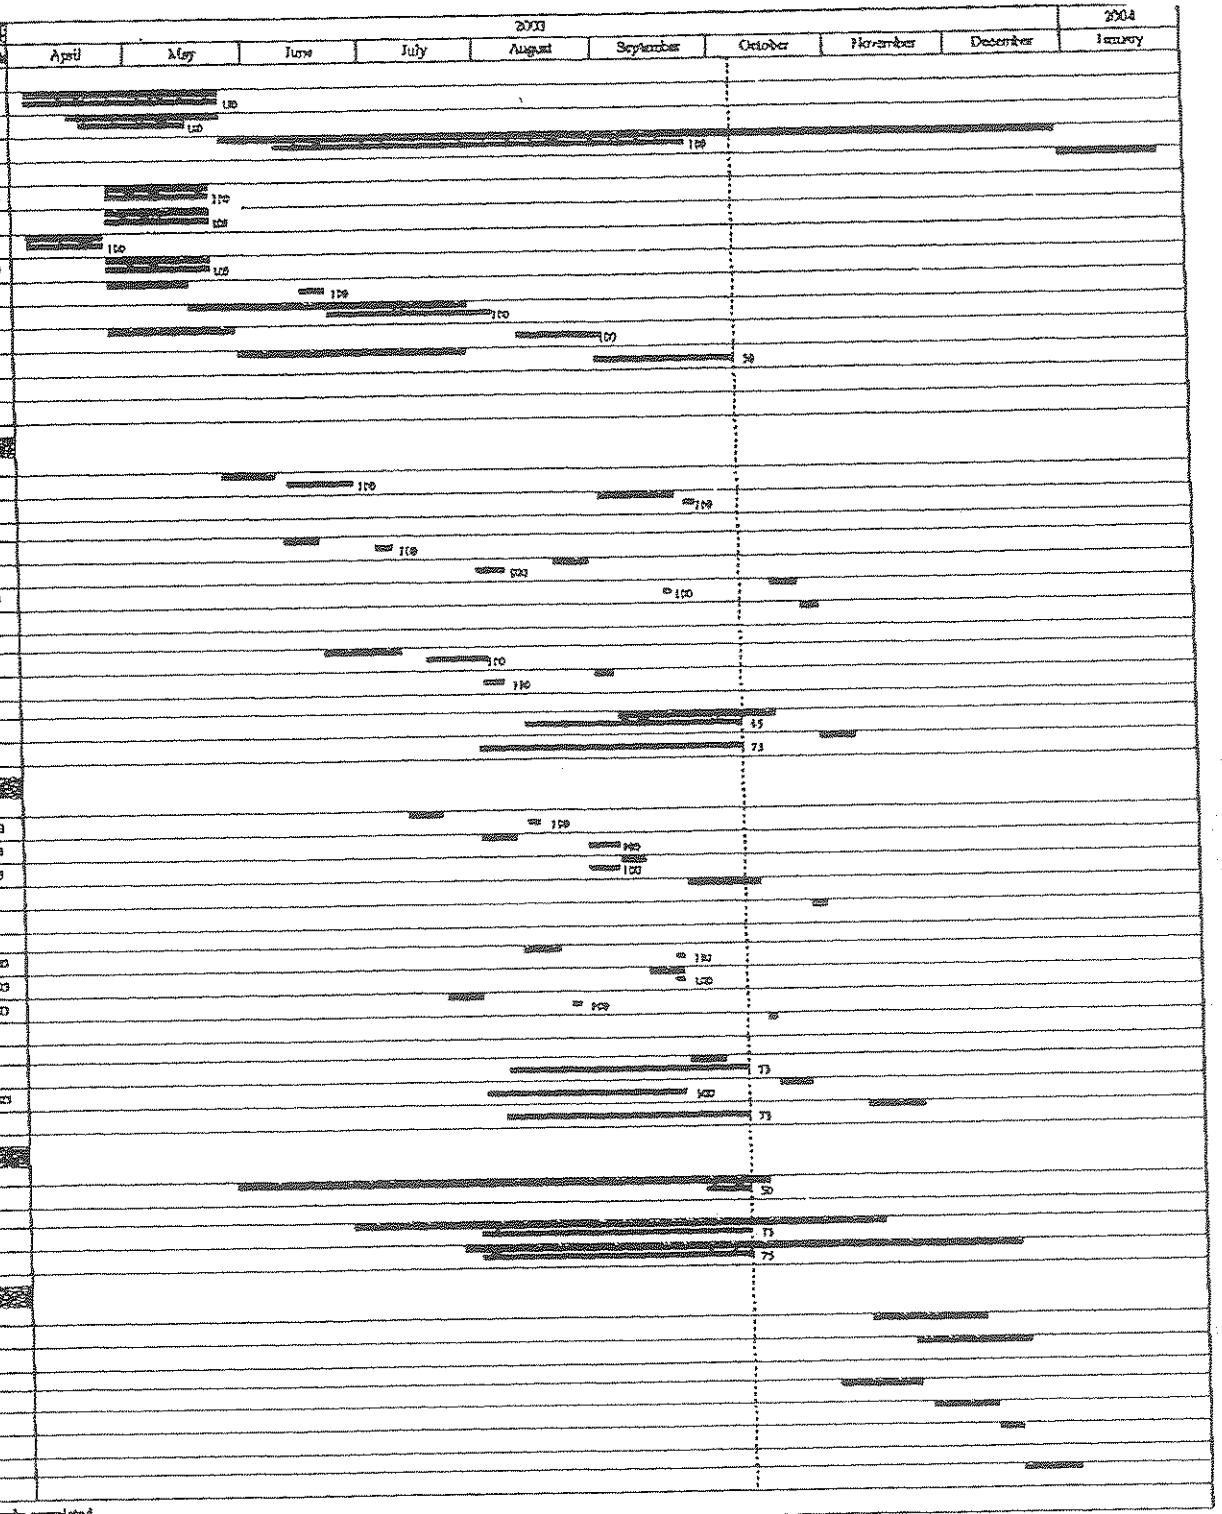

Mid 10
