Appendix 1-1

Construction Programme

ID	Description	Start	End
100	**Salisbury road to FMPHQ**	Mar-05	Nov-07
101	Utilities diversion	Mar-05	May-05
102	Temp wall & decking	Jun-05	Mar-06
103	Excavation works	Apr-06	Oct-06
104	Construction works	Nov-06	Jul-07
105	Backfilling & reinstatement	Aug-07	Nov-07
200	**Underneath FMPHQ to Retrieval Shaft**	Apr-06	Feb-07
203	Mined tunnel	Apr-06	Feb-07
300	**TBM Retrieval Shaft**	Mar-05	Jun-07
301	Utilities diversion	Mar-05	Jun-05
302	Temp wall & decking	Jul-07	Oct-07
303	Excavation works	Nov-05	Mar-06
304	Deassembling TBM (for one tube)	Sep-06	Oct-06
305	Deassembling TBM (for another tube)	Feb-07	Mar-07
306	Shaft fitout	Mar-07	Apr-07
307	Backfilling & reinstatement	May-07	Jun-07
500	**Canton Road Plant Building (CRPB)**	Mar-05	Nov-07
501	Utilities diversion	Mar-05	Jun-05
502	Temp wall & decking	Jul-05	Dec-05
503	Excavation works	Sep-06	Nov-06
504	Construction of CRPB	Feb-07	Jun-07
505	Backfilling & reinstatement (shaft near CHKC)	Jul-07	Sep-07
506	Fitout	Oct-07	Nov-07
600	**Bored Tunnelling**	Jul-05	Jan-07
601	Ground treatment	Jul-05	May-06
602	Diaphragm wall in launching shaft	Jun-05	Jul-05
603	Excavation in launching shaft	Aug-05	Feb-06
604	Assembling TBM in launching shaft	Mar-06	Oct-06
605	Operation in launching shaft (for one tube)	Jun-06	Aug-06
606	Operation in launching shaft (for another tube)	Nov-06	Jan-06
607	Foundation	Jun-06	Jan-07
608	Construction of station box	Feb-07	Mar-07
700	**WKN Station**	Apr-05	Dec-07
701	Utilities diversion	Apr-05	Jul-05
702	Diaphragm wall	Aug-05	May-06
703	Bored piling	Aug-05	May-06
704	Excavation works	Nov-05	Sep-06
705	Construction works	Mar-06	Sep-07
706	Fitout (E&M only)	Dec-06	Dec-07
800	**Tunnels from WKN station to NAC overrun**	Apr-05	May-07
801	Utilities diversion	Apr-05	Jun-06
802	Diaphragm wall	Jul-05	Oct-06
803	Excavation works	Oct-05	Jan-07
804	Construction works	Jan-06	Mar-07
805	Backfilling & reinstatement	Mar-06	May-07

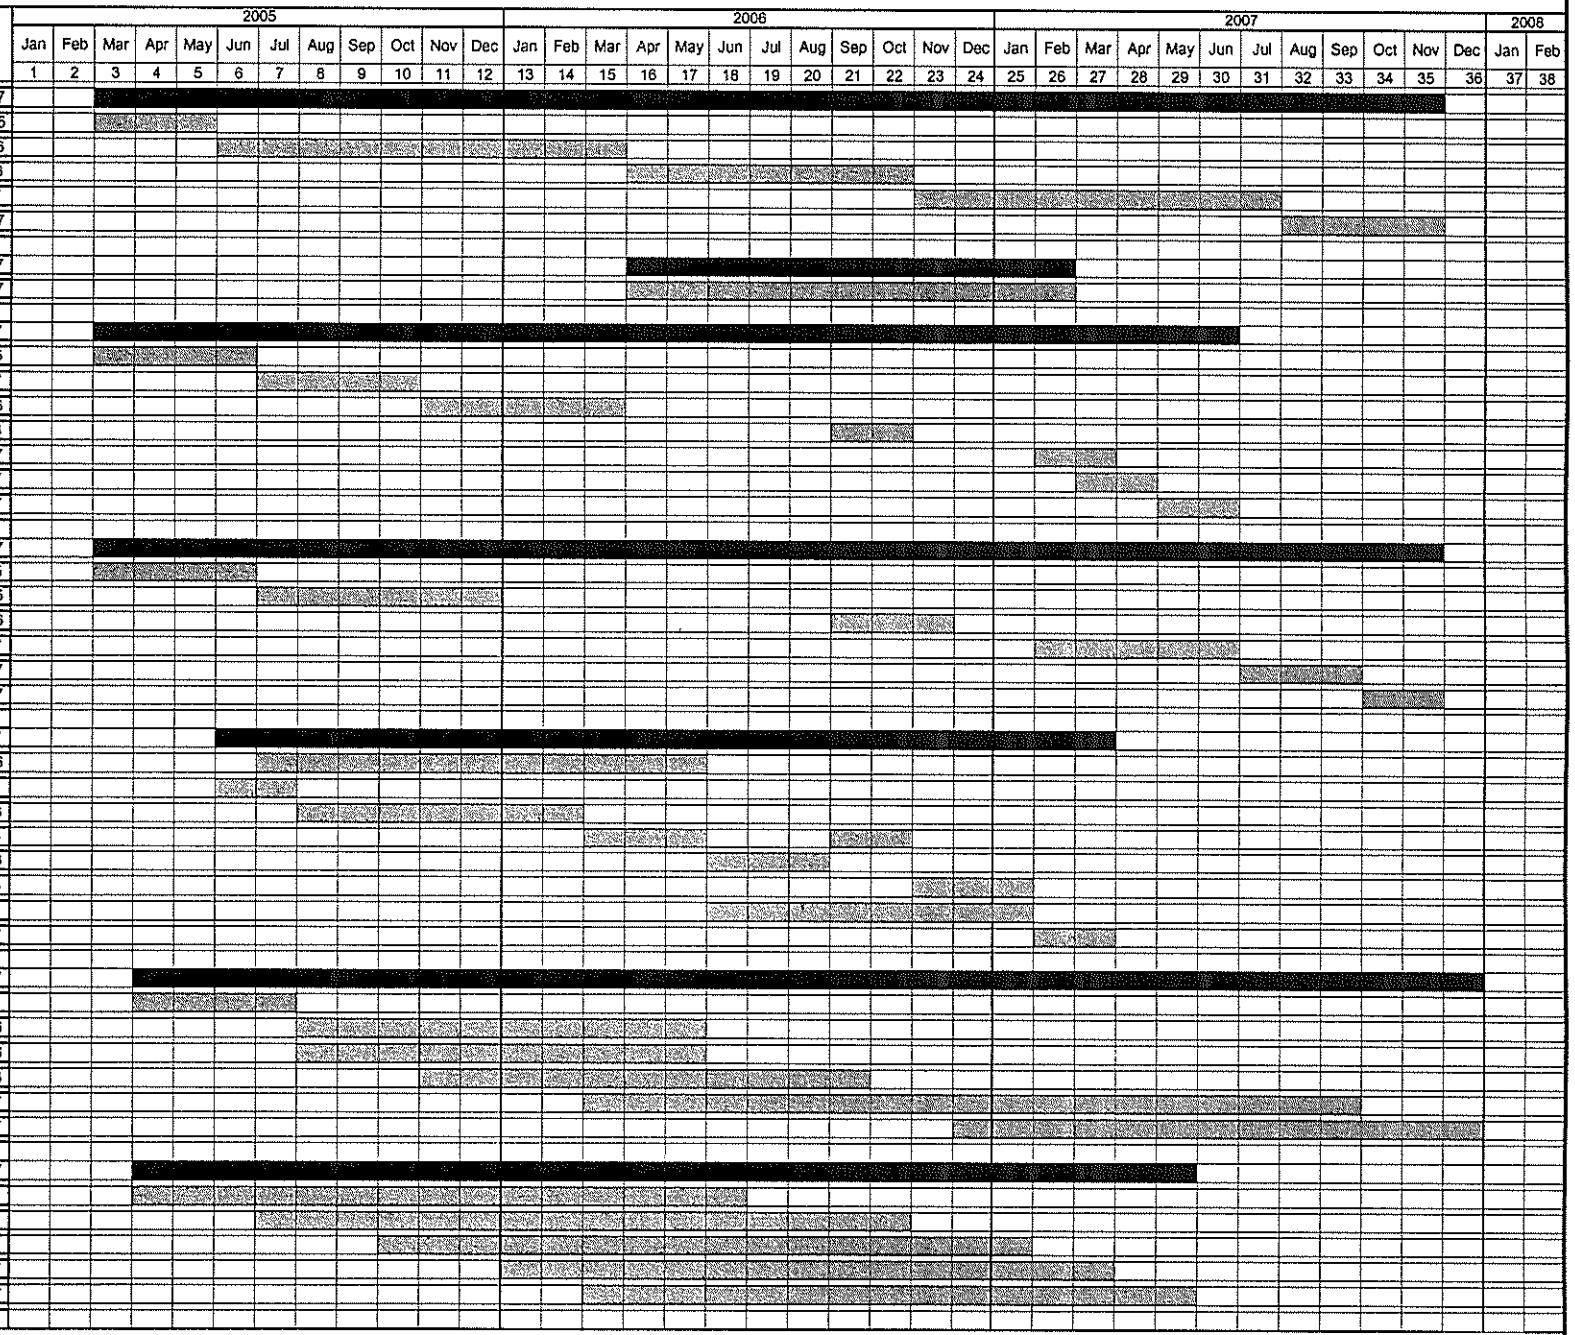

Construction Programme
