Location	Construction Task	Target Start	Target Finish	Orignial Duration (Month)
North Point				
PTW	Drop Shaft	Feb-09	Jun-13	28
	PTW Upgrading	Oct-10	Dec-13	39
NP-viii	Production Shaft	Feb-09	Mar-10	14
	Tunnel J	Apr-10	Sep-13	42
	Construction of Barging Point	Feb-09	Nov-09	5
Wan Chai East				
PTW	Drop Shaft	Feb-09	Sep-13	36
	PTW Upgrading	Jan-11	Dec-13	36
WCE-i	Production Shaft	Feb-09	Mar-10	14
	Tunnels K / J	Apr-10	Sep-13	42
Central				
PTW	Drop Shaft	Feb-09	Jun-13	19
	PTW Upgrading	Sep-10	Jun-13	34
Sai Ying Pun				
SYP-SCC	Production/Junction Shaft	Jun-09	Sep-13	13
	Tunnels M	Jul-10	Feb-13	32
SYP-I	Production/Permanent Shaft	Feb-09	Sep-13	13
	Tunnel K / L	Feb-10	Feb-13	37
	Construction of Barging Point	Feb-09	Nov-09	9
Sandy Bay				
SB-PS	Production / Drop Shaft	Jun-09	Sep-13	12
	Tunnels N / P	Jun-10	Dec-12	31
SB-i	Production Shaft	Jun-09	May-10	12
	Tunnel M	Jun-10	Sep-13	40
	PTW Upgrading	Sep-10	Dec-13	40
Cyberport				
PTW	Production/Drop Shaft	Jun-09	Sep-13	22
	Tunnels N / P	Jul-10	Dec-12	30
	PTW Upgrading	Mar-11	Dec-13	34
	CEPT Demolition	May-14	Oct-14	6
Wah Fu				
PTW	Drop Shaft	Jun-09	Jun-13	19
	PTW Upgrading	Sep-10	Dec-13	40
Aberdeen				
PTW	Drop Shaft	Jun-09	Sep-13	21
	PTW Upgrading	Sep-10	Dec-13	40
	Tunnel Q	Jun-09	Sep-13	52
Abd-iii	Productoin Shaft	Jun-09	Feb-10	9
	Tunnel P	Mar-10	Sep-13	43
Ap Lei Chau				
PTW	Drop Shaft	Jun-09	Sep-13	52
	PTW upgrading	Sep-10	Dec-13	40
Stonecutters Island STW				
SCISTW	Riser Shaft	Feb-09	Sep-13	49
	Civil Works on SCISTW & Disinfection Facilities Site	Sep-10	Feb-14	42
	Production Shaft	Feb-09	Jan-10	12
	Tunnel L	Feb-10	Sep-13	44

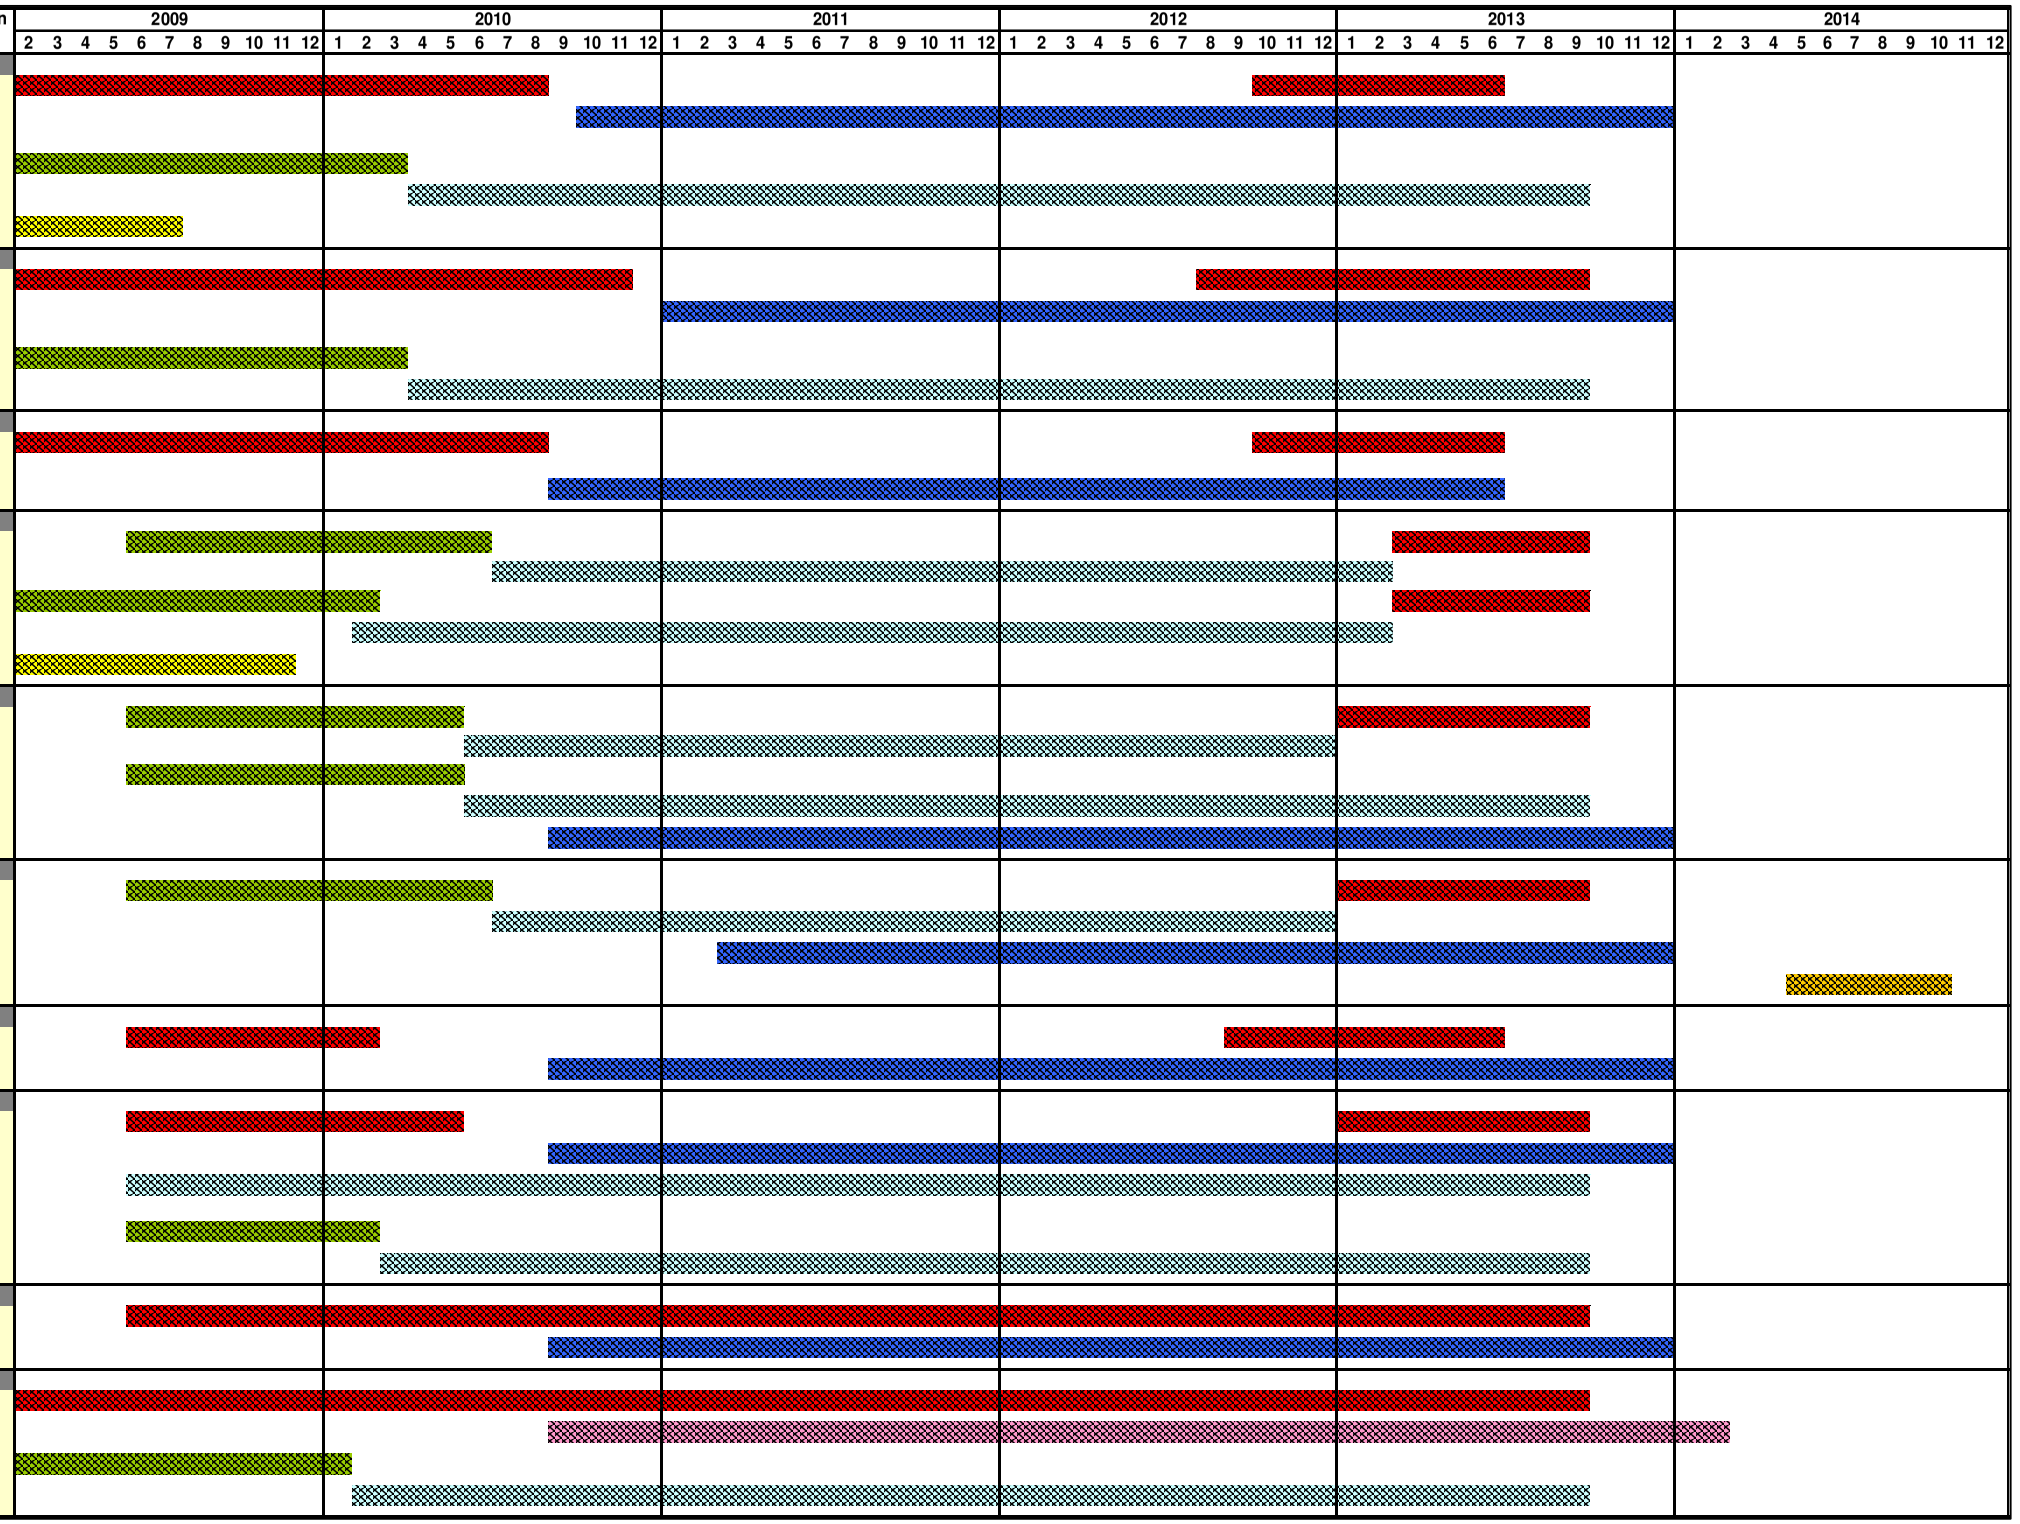

ENSR | AECOM

AGREEMENT NO. CE 43/2005 (EP)

HARBOUR AREA TREATMENT SCHEME (HATS) STAGE 2A ENVIRONMENTAL IMPACT ASSESSMENT STUDY - INVESTIGATION

TENTATIVE CONSTRUCTION PROGRAMME

SCALE	N.T.S.	DATE	Jan-08
CHECK	CGLW	DRAWN	IWSL
JOB NO.	60017198	FIGURE No. 1.3	Rev -

P:/60017198/REPORT/EIA/DRAFT EM&A_V1/FIG/S1/1.3.xls
