MTR Corporation Limited

HONG KONG SECTION OF GUANGZHOU – SHENZHEN – HONG KONG EXPRESS RAIL LINK

(No. EP-349/2009/B)

Environmental Monitoring and Audit Report No. 14

(April 2011)

Verified by:	
Position:	Independent Environmental Checker
Date:	17 May 2011

MTR Corporation Limited

HONG KONG SECTION OF GUANGZHOU - SHENZHEN - HONG KONG EXPRESS RAIL LINK

(No. EP-349/2009/B)

Environmental Monitoring and Audit Report No. 14


(April 2011)

Certified by: Glenn Fronmer

Position: Environmental Team Leader

Date: 13 MAY 2011

Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link

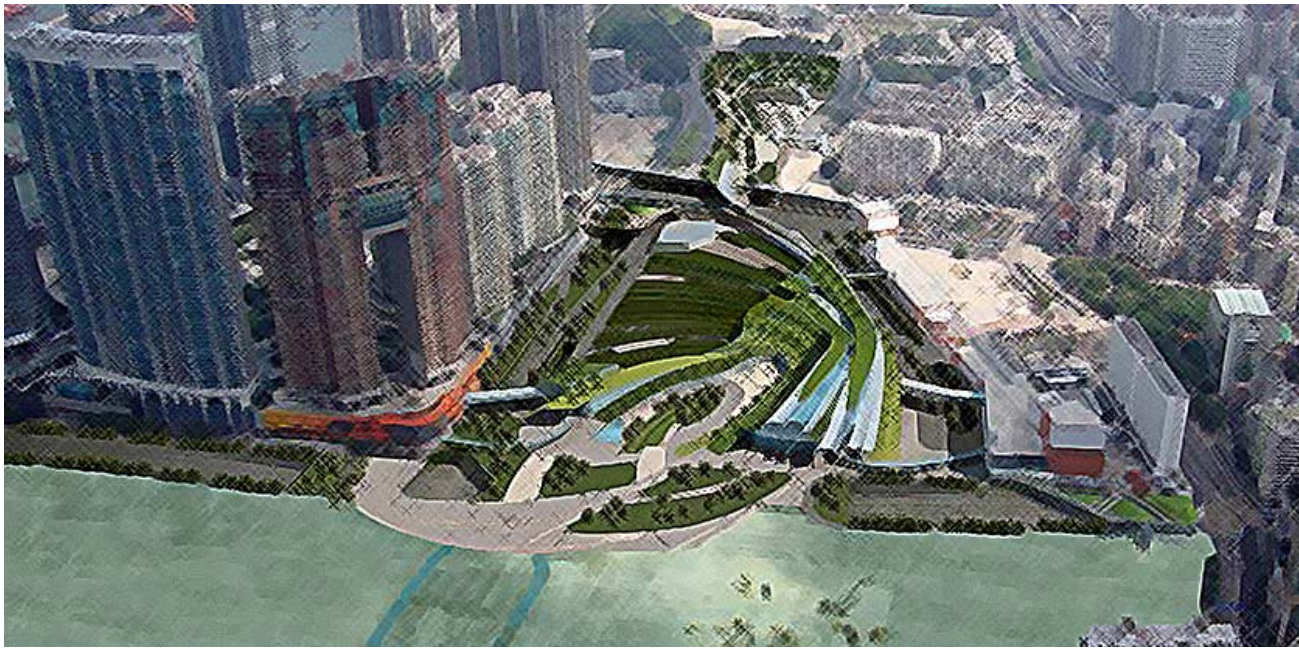

Environmental Monitoring and Audit Report

April 2011

EXECUTIVE SUMMARY

This is the 14th monthly Environmental Monitoring and Audit (EM&A) Report presenting the EM&A works undertaken during the period from 1 to 30 April 2011 for the Hong Kong Section of Guangzhou - Shenzhen - Hong Kong Express Rail Link (hereinafter referred to "the XRL" or "the Project") in accordance with the EM&A Manual and the requirement under EP-349/2009/B.

Air Quality

Air quality monitoring was conducted for 24-hour Total Suspended Particulates (TSP) at 17 air quality monitoring locations in the vicinity of Works Area in Mai Po (Works Area A) Ngau Tam Mei (Works Area B), Tai Kong Po (Works Area C), Shek Kong (Works Area D), Tse Uk Tsuen, (Works Area E), Pat Heung (Works Area F), Shing Mun (Works Area G), Shek Yam (Works Area H), Kwai Chung (Works Area J), Mei Foo (Works Area L), Nam Cheong (Works Area P, Q and R) and West Kowloon (Works Area V1 and V2) in April 2011.

Please refer to the section "Environmental Complaints/Exceedance/Non-compliance/ Summons and Prosecution" below for the exceedance in air quality in the reporting month.

Airborne Noise

Airborne noise was measured in terms of $L_{eq\ (30min)}$ dB(A) with L_{10} and L_{90} measurements as reference at 33 noise monitoring locations in the vicinity of Works Area in Mai Po (Works Area A), Ngau Tam Mei (Works Area B), Tai Kong Po (Works Area C), Shek Kong (Works Area D), Tse Uk Tsuen, (Works Area E), Pat Heung (Works Area F), Shing Mun (Works Area G), Shek Yam (Works Area H), Kwai Chung, (Works Area J and K), Mei Foo (Works Area L), Nam Cheong (Works Area M, N, O, P, Q, R, S and T) and West Kowloon (Works Area V1 and V2) once every week.

Please refer to the section "Environmental Complaints/Exceedance/Non-compliance/ Summons and Prosecution" below for the noise exceedance in the reporting month.

Monitoring of Avifaunal Species

Weekly ecological monitoring was conducted during the period of hoarding erection at Shek Kong Stabling Sidings (SSS-2a). Monthly ecological monitoring was conducted during the construction of Mai Po Ventilation Building Works Area (MPV), access road to Tai Kong Po Works Area (TPP-1/2/3), Shek Kong Stabling Sidings (SSS-3), Pat Heung Ventilation Building Works Area (PHV-1) and Tse Uk Tsuen (TUW-1/2). The monitoring results indicated the survey areas were utilized by a large number of waterbirds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed for the survey areas. Based on the monitoring results, no adverse indirect impacts arising from the Project were observed.

Monitoring of Impact at Fishpond due to Noise

In accordance with the Monitoring and Emergency Response Plan, impact noise monitoring was conducted at fish pond on weekly basis for assessment of impact at fishponds due to noise. It was revealed from the monitoring results that all monitoring results were within the Limit Level. Based on the monitoring results, there was no adverse impact at fishpond due to noise.

Landscape and Visual

Regular inspections and audits conducted by certified Arborist found that the tree protection works being carried out by the civil works and transplanting contractors were in accordance with the requirements of EP and EIA.

Environmental Audits

In this reporting month, regular site inspections attended by representative from MTRCL and Contractors were carried out at 803A, 803B, 803D, 810B, 811A and 811B in West Kowloon, 802, 805 and 820 in Nam Cheong, 821 in Kwai Chung, 822 in Pat Heung, Shing Mun, Shek Yam, Tai Shu Ha Road West Magazine Site, So Kwun Wat Nursery and Magazine Site and Tsing Chau Tsai Barging Point, 823A and 823B in Shek Kong, Tse Uk Tsuen, To Kau Wan stockpiling facility, 824 in Ngau Tam Mei and Tai Kong Po and 825 in Mai Po and Siu Lam Barging Point. In addition to the regular site inspections, IEC environmental audits attended by IEC, MTRCL

and Contractors were held on monthly basis. Issues observed during these audits are detailed in Section 6.

Environmental Complaints / Exceedance / Non-compliance / Summons and Prosecution

For the reporting month, a total of 5 environmental complaints were referred from EPD. The environmental complaints received were related to construction noise from construction site near Hoi Fai Road; generation of muddy water from WKT works area; generation of mud stain from works area near Man Yui Street; construction noise from WKT works area near Sorrento; construction noise from WKT Works Area near Austin Station. Complaint investigations were conducted in accordance with the complaint handling procedure in the EM&A Manual. Details of complaints are contained in Section 7.

For the reporting month, noise exceedances of air-borne noise Limit Level were recorded at Kong Tai Road Village House (CN 5), HKIVE Haking Wong Waterfront Annex (CN 23), St. Mary's Church Mok Hing Yiu College (CN 25), The Waterfront (CN 32) and The Arch (CN 33). There were two noise exceedances of Action Level triggered due to complaint during daytime hours in the reporting month. Actions stipulated under the Event and Action Plan (Table 3.4 of the EM&A Manual) was implemented. Noise source was identified and the contractor had implemented further mitigation measures accordingly to minimize the noise impact.

Exceedances of 24-hour TSP Action Level were recorded at Kong Tai Road Village House (AM3), DD110 LOT 482, Wang Toi Shan (AM 4), between Sorrento and The Waterfront (AM 15) and The Victoria Towers (AM 17). In addition, no exceedance of 24-hour TSP Limit Level was recorded. Actions stipulated under the Event and Action Plan (Table 9.4 of the EM&A Manual) were implemented. Investigation was carried out with dust source identified and the contractor implemented further mitigation measures accordingly to minimize the dust impact.

No non-compliance event was recorded during the reporting period. No summons/prosecutions was received in this reporting period.

Works for Coming Month

Construction works were started in Works Areas A, B, C, D, D1, E, F, G, H, J, L, M, N, O, P, Q, R, S, U, V1, V2, Y, Z, AA, AC, AE and AG.

Please refer to Table 8-1 for the major works in the respective works areas. Impact monitoring would be continued in coming reporting month accordingly with reference to the EM&A Manual.

Further Environmental Key Issues

Air quality, airborne noise at NSRs and fishpond, ecological, landscape and visual monitoring shall continue in the following month. Considering the nature of construction activities, key environmental issues in the coming months include the followings:

- Disposal of C&D waste;
- Dust generation from site activities;
- Noise impact from operating equipment;
- Site water discharge;
- Chemical wastes;
- Ecological impact;
- Trees protection

Reporting Changes

In the reporting period, there was no reporting change of circumstances which may affect the compliance with the recommendations of the EIA Report.

Table of Contents

EXECUTIVE SUMMARY 1

1. INTRODUCTION 5

2. PROJECT INFORMATION 7

3. ENVIRONMENTAL STATUS 11

4. SUMMARY OF EM&A REQUIREMENT 19

5. MONITORING RESULT 32

6. SITE INSPECTION 56

7. NON-COMPLIANCE AND DEFICIENCY 64

8. FUTURE KEY ISSUES 68

9. CONCLUSIONS 73

Appendix

Appendix A Works Area

Appendix B Project Management Organization and Contacts of Key Personnel

Appendix C Implementation Status

Appendix D Monitoring Locations

Appendix E Monitoring Schedule

Appendix F Graphical Plots of Monitoring Results

Appendix G Bird Species and Abundance Recorded during Avifauna Survey

Appendix H Representative Photographs of the Avifauna Monitoring

Appendix I Certified Arborist Inspection Record

Appendix J Landfill Gas Monitoring Record at Rambler Channel Barging Point

1. INTRODUCTION

1.1 Project Background

Further to the Government's decision made in April 2008, MTR Corporation (MTR) commenced to plan and design the Hong Kong Section of Guangzhou - Shenzhen - Hong Kong Express Rail Link (hereinafter referred to "the XRL" or "the Project"), which is a committed cross boundary transport infrastructure project.

The XRL would provide high speed rail services between Hong Kong and Guangzhou, and a connection to the national high-speed passenger rail network serving major mainland cities outside of Guangdong province. The Hong Kong section of the XRL is about 26km from new terminus located in West Kowloon (i.e. West Kowloon Terminus (WKT)) to the boundary at Huang gang. Along the railway corridor, there would be a total of eight ventilation buildings/ emergency access point (EAP), stabling sidings and a maintenance facility at Shek Kong Stabling Sidings (SSS) and an Emergency Rescue Station (ERS) next to SSS serving the operation of the XRL.

1.2 Coverage

This is the 14th monthly Environmental Monitoring and Audit (EM&A) Report presenting the EM&A works undertaken during the period from 1 to 30 April 2011 for XRL in accordance with the EM&A Manual and the requirement under Environmental Permit No. EP-349/2009/B.

2. PROJECT INFORMATION

2.1 Project Management Organisation and Management Structure

The project management organisation chart and contact of key personnel are shown in Appendix B.

2.2 Construction Activities

This report marked the 14th month of civil construction in Works Area A, B, C, D, D1, E, F, G, H, J, L, M, N, O, P, Q, R, S, U, V1, V2, Y, Z, AA, AC, AE and AG for April 2011. It is anticipated that the civil construction be completed in year 2015. The updated construction activity is provided in Section 8. Major construction activities undertaken in the reporting month is summarized in the following table.

Contract	**Works Area**	**Major Construction Activities**
Nam Cheong		
802	Q	Sheet-pilling, pre-drilling work, bored pile removal, H-pile extraction, pile cap demolition, excavation & lateral supports and utility diversion
805	N,O	Piers removal of footbridge, sheet piling works and pile removal at CLP Spare Equipment Building
805	S	Demolition of pile cap and sheet piling work
West Kowloon		
803A	V1	Diaphragm wall construction, remedial works, concrete coring, utilities diversion and road works
803B	V1	Socketed H-piling works, pre-drilling, Loading test, Bored piling and interface coring for bored piles
803D	V1	Diaphragm wall, loading test, remedial works and concrete coring

Contract	**Works Area**	**Major Construction Activities**
810B	V1 & U	Site Clearance, Construction of Site Office, Site Establishment, Hoarding Erection, Predrill bore piles and Excavation along Lin Cheung Road and Austin Road West.
811A	V2	Construction of diaphragm wall, H-pile and bored piles; traffic diversion at Lai Cheung Road; construction of traffic deck at Lai Cheung Road; external works to CLP Sub Station at Lai Cheung Road
811B	V2	Construction for diaphragm wall, bored piling and H-piles, temporary road construction, construction of temporary footbridge; culvert diversion
820	V2	Ground treatment
Nam Cheong		
811B	Y	Operation of Nam Cheong Barging Point
820	M	Utility diversion; Removal of pile by hydraulic rotator on-going.
820	P	Grouting work on-going; shaft excavation at Box A D-wall, strut installation at Box A D-wall, excavation and concreting for Box B D-wall, utilities diversion, temporary traffic arrangement, pre-bored H-pile at Box B, pile removal works
820	R	Preparation work for pile-removal; Temporary traffic arrangement and utilities diversion
820	S	Temporary traffic arrangement; Utilities diversion; Removal of pile by hydraulic rotator.
820	Y	Disposal ramp erection; Plant mobilization and site set-up

Contract	**Works Area**	**Major Construction Activities**
821	Y	Pipe-work setting for the barging point, stockpiling and barging activities
Mei Foo		
820	L	Nil
Kwai Chung		
821	J	Establishment of workshop area, blasting, breaking and drilling work inside the portal of the tunnel, stockpiling, transportation of excavated materials to Barging Point
Pat Heung		
822	F	Vent adit access and portal excavation works; Pipe piling; Retaining wall construction
Shek Yam		
822	H	Adit Construction, preparation work of conveyor erection
Shing Mun		
822	G	Pipe piling, utility diversion
So Kwun Wat		
822	AC	Nil
Tai Shu Ha Road West Magazine Site		
822	AE	Nil
Tsing Chau Tsai Barging Point		
822	AG	Nil

Contract	Works Area	Major Construction Activities
Shek Kong Stabling Sidings		
823A& 823B	D and D1	Site formation, pre-drilling works, establishment of site office and stockpiling area
Tse Uk Tsuen		
823A	E	Pre-drilling works, construction of haul road
Rambler Channel Barging Point		
823B	Z	Site formation, establishment of wheel washing facilities
To Kau Wan Works Area		
823B	-	Nil
Ngau Tam Mei		
824	B	Bored piling works
Tai Kong Po		
824	C	Pipe piling works for construction of additional circular shaft and main shaft within Tai Kong Po Works Area; bridge construction at access road
Mai Po		
825	A	Shaft construction
Siu Lam Barging Point		
825	AA	Nil

Table 2-1 Major construction activities in April 2011

3. ENVIRONMENTAL STATUS

3.1 Status of Implementation of mitigation measures

Environmental mitigation measures recommended in the EIA report were implemented and their implementation status are summarized in Appendix C.

3.2 Status of Submissions under EP

A summary of the submissions submitted under the EP for this Project during the reporting month is presented in Table 3-1 below:

EP-349/2009/B Clause No.	**Document Title**
2.11	Groundwater Monitoring and Contingency Plan for North Section of Approach Tunnel (Contract 811B) (Rev B)
2.21	Supplementary Contamination Assessment Report and Remediation Action Plan for Kwai Chung Ventilation Building Works Area (Rev C) – Addendum Page
2.42	Baseline Monitoring Report (Part 13) Rev 2
2.46	Monthly EM&A Report

Table 3-1 Summary of the status of submissions submitted under the EP in the reporting month

3.3 Status of Permit/License/Notifications

A summary of the status of permits, licences and notifications on environmental protection made, applied or approved under this Project during the previous and reporting month is presented in Table 3-2 below. The Environmental Permit No. EP-349/2009/B issued by EPD was used for the XRL project.

Item	Item Description	Application Date	Permit Status
Contract 802 (Works Area Q)			
1	Construction Noise Permit	19 Apr 2011	Acknowledged on 21 April 2011 (Ref. No.:329295) Pending for EPD's approval
2	QPME application Mobile Crane (Model: SCX900HD-2C3, Serial No.: SC09D-7004)	10 Mar 2011	EPD's acknowledgement ref. no.: (2) in QPME/0039-11 dated 10 Mar 2011 EPD approved on 6 April 2011 (QPME ID Code: EPD-01118)
3	QPME application Mobile Crane (Model: SCX1200-2C3, Serial No.: SC120-7182)	10 Mar 2011	EPD's acknowledgement ref. no.: (2) in QPME/0040-11 dated 10 Mar 2011 EPD approved on 6 April 2011 (QPME ID Code: EPD-01119)
4	QPME application Excavator (Model: Cat 320d, Serial No.: CAT0320DHAZR03079)	16 Mar 2011	EPD's acknowledgement ref. no.: (2) in QPME/0051-11 dated 21 Mar 2011 EPD approved on 15 April 2011 (QPME ID Code:

Item	Item Description	Application Date	Permit Status
			EPD-01145)
Contract 803A (Works Area V1)			
1	WPCO license (variation)	15 Apr 2011	In progress
Contract 803B (Works Area V1)			
1	Construction Noise Permit for Area 13.37	21 Feb 2011	Approved on 2 Mar 2011 (Permit no. GW-RE0131-11 valid till 10 Aug 2011)
Contract 803D (Works Area V1)			
1	WPCO License (variation)	15 Apr 2011	In progress
2	Construction Noise Permit - Renewal	1 Apr 2011	Approved on 15 Apr 2011 (Permit no. GW-RE0265-11 valid till 13 Oct 2011)
Contract 805 (Works Area S, N, O)			
1	CNP for Pile Removal works at Sham Mong Road	17 Mar 2011	Refused by the EPD on 24 Mar 2011.
Contract 810B (Works Area V1 & U)			
1	Dumping Permit for Types 1 & 2 Marine sediment	3 Mar 2011 and 12 Apr 2011	Approved on 25 Mar 2011 (Permit Nos. EP/MD/11-157 (Type 1) valid from

Item	Item Description	Application Date	Permit Status
			28/03/2011 to 27/09/2011) & EP/MD/11-158 (Type 2) valid from 28/03/2011 to 27/04/2011
2	WPCO License (variation to add discharge points)	12 Apr 2011	Under Assessment
Contract 811A (Works Area V2)			
1	Construction Noise Permit (for relocation of gantry)	11 Feb 2011	Approved on 3 Mar 2011 (Permit no. GW_RE0077_11 valid till 21 April 2011)
2	Construction Noise Permit (Works Area 13.46 &13.44)	11 Mar 2011	Approved on 29 Mar 2011 (Permit no. GW_RE0214_11 valid till 26 June 2011)
Contract 811B (Works Area V2 & Y)			
1	Construction Noise Permit (for erection of temp. steel bridge at area 13.62)	10 Mar 2011	License no.: GW-RE-0195-11 Valid from 25 Mar 11 to 30 Jun 11
2	Construction Noise Permit (for the	11 Mar 2011	License no.:

Item	Item Description	Application Date	Permit Status
	loading/unloading of spoil activities at the Nam Cheong Barging Point)		GW-RE0209-11 Valid from 26 Mar 11 to 23 Sep 11
3	Construction Noise Permit (Renewal Permit GW-RE0641-10)	24 Mar 2011	License no.: GW-RE0243-11 Valid from 13 Apr 11 to 5 Oct 11
4	Registration as Chemical Waste Producer (site areas include 13.42A, 13.42B, 13.42C, 13.41AA, 13.41AB, 13.38, 13.41C & 13.62)	11 Feb 2011	Registration no. WPN 5213-225-G2522-02 Valid on 14 Mar 2011
5	Registration as Chemical Waste Producer (Nam Cheong Barging Point)	11 Feb 2011	Registration no. WPN 5213-269-G2534-01 Valid on 17 Mar 2011
6	WPCO license 13.41A, 13.41C & 13.62 (site area)	10 Mar 2011	License no.: WT00008728-2011 Valid from 19 Apr 11 to 30 Apr 16
7	Construction Noise Permit (for the loading/unloading of spoil activities to barge at the Nam Cheong Barging Point)	1 Apr 2011	Licence no.: GW-RE0268-11 Valid from 14 Apr 11 to 13 Oct 11
Contract 821 (Works Area J, Y)			
1	Construction Noise Permit	25 Mar 2011	Permit GW-RW0245-11 had

Item	Item Description	Application Date	Permit Status
	(24 hour Construction Work at Tai Lin Pai Road J/O Wing Yip Street, Kwai Chung, N.T.)		been granted. Valid from 8 Apr 2011 to 7 Oct 2011
2	Construction Noise Permit (Operation of Barging Point (up to 2300hr))	31 Mar 2011	Permit GW-RW0266-11 had been granted. Valid from 15 Apr 2011 and will be expired on 11 Oct 2011
Contract 822 (Works Area F, G, H, AC, AE and AG)			
1	Construction Noise Permit for PME operation at Works Area H	4 Mar 2011	License No. GW-RW0179-11, Valid 18 Mar 2011 to 31 Aug 2011 for Works Area H
2	Specified Process License for Rock Crusher at Works Area H	11 Mar 2011	Under Assessment
3	Construction Noise Permit for Road Re-surfacing Works at Works Area G from 19:00 to 07:00 next day on any day not being a general holiday.	19 Apr 2011	Acknowledge receipt (Ref. No. 329228)
Contract 823A *(Works Areas D, D1 and E)*			
1	WPCO license for Works Area D1 at Nam Hing West Road Site	21 Jan 2011	License granted on 29 Mar 2011. (License no.

Item	Item Description	Application Date	Permit Status
			WT000008675-2011 valid until 31 Mar 2016)
Contract 823B (Works Area D, To Kau Wan Works Area)			
1	Construction Noise Permit For generator operation at Works Area 4.8	12 Apr 2011	Permit GW-RN011411-11 had been granted. Valid to 15 Oct 2011
Contract 824 (Works Area B and C)			
1	WPCO License for Works Area B	8 Dec 2010	License granted on 21 Mar 2011 (License no.: WT00008723-2011 valid to 31 Mar 2016)
2	Registration as Chemical Waste Producer	11 Oct 2010	Approved on 23 Mar 2011 (Registration no. WPN:5213-532-K2992-01)
3	Construction Noise Permit for the use of PMEs other than Percussive Piling for Works Area B	23 Mar 2011	Permit granted on 31 Mar 2011 (Permit no.: GW-RN0106-1 valid to 6 Oct 2011)
4	Construction Noise Permit for the use of PMEs other than Percussive Piling for	29 Apr 2011	Under Assessment

Item	Item Description	Application Date	Permit Status
	Works Area B		
5	Construction Noise Permit for the use of PMEs other than Percussive Piling for Works Area C	20 Apr 2011	Under Assessment
Contract 825 (Works Area A)			
1	Construction Noise Permit for welding	28 Feb 2011	Permit granted on 7 Mar 2011 (Ref: GW-RN0077-11)

Table 3-2 Summary of the status of permits, licences and notifications made, applied and approved under this Project during the previous and reporting month

4. SUMMARY OF EM&A REQUIREMENT

4.1 Air Quality

4.1.1 Air Quality Parameters

In accordance to the EM&A Manual, 24-hour Total Suspended Particulates (TSP) levels were measured at the 17 air monitoring locations in accordance with the EM&A Manual. Monitoring was undertaken at each monitoring location once per every 6 days. Information such as date of monitoring, duration, weather condition, equipment used and monitoring results shall be recorded on the field data sheet developed for the Project. Monitoring results are summarized in Section 5.

4.1.2 Monitoring Methodology and Calibration

Monitoring was undertaken to establish for 24-hour Total Suspended Particulates (TSP) at 17 monitoring locations in the vicinity of the Works Area A, B, C, D, E, F, G, H, J, L, P, Q, R, V1 and V2. Monitoring of 24-hour TSP was carried out using a high volume sampler (HVS) according to Part 50 Chapter 1 Appendix B, Title 40 of the Code of Federal Regulations of the USEPA.

The sampling procedure follows to that described Part 50 Chapter 1 Appendix B, Title 40 of the Code of Federal Regulations of the USEPA. TSP is sampled by drawing air through a conditioned, pre-weighed filter paper inside the high volume sampler at a controlled rate. After 24-hour sampling the filter paper with retained particles shall be collected and returned to HOKLAS accredited laboratory (ALS Technichem (HK) Pty Ltd) for drying in a desiccators followed by accurate weighing. TSP levels are calculated from the ratio of the mass of particulate retained on the filter paper to the total volume of air sampled.

The flow rate of the high volume sampler with mass flow controller was calibrated using an orifice calibrator. Initial calibration (five points) was conducted upon installation and prior to commissioning. Calibration was carried out every six months. the detail of calibration is shown in Table 4-1 below. The samplers shall be properly maintained. Prior to dust monitoring commencing, appropriate checks shall be made to ensure that all equipment and necessary power supply are in good working

condition.

Monitoring Station ID	Air Quality Monitoring Location	HVS Serial Number	Last Calibration Date
AM 1	Outside No. 142 Mai Po San Tsuen	467	10/1/2011
AM 2	Yau Tam Mei Village House	468	27/4/2011
AM 3	Kong Tai Road Village House	510	27/4/2011
AM 4	DD110 LOT 482, Wang Toi Shan	521	25/1/2011
AM 5	Leung Uk Tsuen Squats	1276	25/1/2011
AM 6	630 Sheung Tsuen	469	25/1/2011
AM 7	Tse Uk Tusen	1763	25/1/2011
AM 8	No. 306, Sheung Tsuen San Tsuen Village House	520	27/4/2011
AM 9	Sau Shan House, Cheung Shan Estate	529	29/12/2010
AM 10	Yau Ma Hom Resite Village	509	29/12/2010
AM 11	Chung Shun Knitting Centre	1707	15/02/2011
AM 12	Po Leung Kuk Tong Nai Kan College	520	6/12/2010
AM 13	St. Andrew Primary School	524	28/1/2011

Monitoring Station ID	Air Quality Monitoring Location	HVS Serial Number	Last Calibration Date
AM 14	Yaumati Catholic Primary School	407	28/1/2011
AM 15	Between Sorrento and The Waterfront	515	6/12/2010
AM 16	Tower 3, The Waterfront	1282	6/12/2010
AM 17	The Victoria Towers	528	6/12/2010

Table 4-1 Calibration details of HVS

4.1.3 Monitoring Location

According to the EM&A Manual, air quality monitoring was carried out at the locations as shown in Table 4-1 above. The monitoring locations are illustrated in Appendix D.

4.1.4 Action and Limit Levels

With reference to the baseline monitoring results, the Action and Limit Levels for the 24-hour TSP monitoring derived are shown in Table 4-2. In the case of exceedance of Action and/or Limit levels for air quality occur, the Event and Action Plan as stipulated the EM&A Manual shall be implemented.

Monitoring Station ID	24-hour TSP Level in μg/m^3	
	Action Level	Limit Level
AM 1	217.3	260
AM 2	179.4	260
AM 3	154.7	260
AM 4	148.6	260

Monitoring Station ID	24-hour TSP Level in μg/m^3	
	Action Level	Limit Level
AM 5	152.0	260
AM 6	145.6	260
AM 7	149.8	260
AM 8	158.1	260
AM 9	171.2	260
AM 10	174.8	260
AM 11	160.3	260
AM 12	162.5	260
AM 13	180.3	260
AM 14	158.2	260
AM 15	168.8	260
AM 16	155.9	260
AM 17	179.3	260

Table 4-2 Action and Limit Levels for Air Quality

4.2 Air-borne Noise

4.2.1 Noise Parameters

In accordance to the EM&A Manual, construction noise monitoring shall be conducted to obtain one set of 30-minute measurement at each monitoring station between 0700 and 1900 hours on normal weekdays at a frequency of once per week when construction activities are underway. The L_{eq}, L_{10} and L_{90} were also recorded at the specified interval.

4.2.2 Monitoring Methodology and Calibration

As referred to the Technical Memorandum (TM) issued under the NCO, sound level

meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. In this baseline monitoring, B&K 2250 sound level meters, which complies with the above-mentioned specifications, were used.

Immediately prior to and following each noise measurement the accuracy of the sound level meter should be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the difference between calibration levels obtained before and after the noise measurement is less than 1.0 dB.

The sound level meters and calibrator are verified by the certified laboratory or manufacturer at a regular interval to ensure they perform to the same level of accuracy as stated in the manufacturer's specifications. Detail of calibration is shown in Table 4-3 below:

Monitoring Station ID	**Noise Monitoring Location**	**Serial Number**	**Last Calibration Date**
Sound Level Meters			
CN 1	No. 142 Mai Po San Tsuen	2701830	28/12/2010
CN 2	Mai Po San Tsuen Village House	2701819	28/12/2010
CN 3	Yau Tam Mei Village House	2718893	21/6/2010
CN 4	Yau Tam Mei Village House	2718887	21/6/2010
CN 5	Kong Tai Road Village House	2718895	21/6/2010
CN 6	Kong Tai Road Village House	2718879	21/6/2010

Monitoring Station ID	Noise Monitoring Location	Serial Number	Last Calibration Date
CN 7	372 Tai Kong Po Tsuen	2718881	21/6/2010
CN 8	DD110 LOT 482, Wang Toi Shan	2718882	21/6/2010
CN 9	Leung Uk Tsuen Village House	2718889	21/6/2010
CN 10	DD110 LOT 482, Wang Toi Shan	2718891	21/6/2010
CN 11	182B, Wang Toi Shan San Tsuen	2718884	21/6/2010
CN 12	DD108, Nam Hing Lei, Wing Hing Wai	2718892	21/6/2010
CN 13	Tse Uk Tsuen	2718883	21/6/2010
CN 14	Tse Uk Tsuen	2718890	21/6/2010
CN 15	No. 305B - Sheung Tsuen San Tsuen Village House	2718885	21/6/2010
CN 16	DD 114 LOT 1405 Sheung Tsuen	2718888	21/6/2010
CN 18	Sau Shan House	2701831	13/1/2011
CN 19	Sun Fung Centre	2701821	10/1/2011
CN 20	VTC Kwai Chung Training Centre Complex	2718894	21/6/2010
CN 21	Po Leung Kuk Tong Nai Kan College	2701820	8/4/2011
CN 22	Block I, Lai Chi Kok Reception Centre	2709427	8/4/2011

Monitoring Station ID	Noise Monitoring Location	Serial Number	Last Calibration Date
CN 23	HKIVE Haking Wong Waterfront Annex	2701818	10/1/2011
CN 24	St. Andrew Primary School	2701825	17/1/2011
CN 25	St. Mary's Church Mok Hing Yiu College	2709428	13/4/2011
CN 26	Ying Wah College	2701822	13/1/2011
CN 27	Cheong Shun House, Nam Cheong Estate	2709426	13/4/2011
CN 28	Tower 6, Harbour Green	2701817	3/1/2011
CN 29	Yaumati Catholic Primary School	2701815	3/1/2011
CN 30	Man Cheong Street Refuse Collection Point	2701816	30/12/2010
CN 31	Tower 6, Sorrento	2701826	17/1/2011
CN 32	Tower 3, The Waterfront	2701823	30/12/2010
CN 33	Star Tower, The Arch	2701827	17/1/2011
CN 34	The Victoria Towers	2701829	6/1/2011
Calibrator			
Serial Number		**Last Calibration Date**	
10186489		23/5/2010	

Table 4-3 Calibration details of noise monitoring equipments

Note:

1. Due to school closure, monitoring at Tsuen Wan Lutheran School (CN 17) was temporarily suspended. Monitoring would be carried out subject to confirmation of noise sensitive use of the

building.

2. A correction factor has been applied at CN19 to take into account the noise barrier effect. The correction factor was agreed with IEC according to Section 3.11 of the EM&A Manual.

4.2.3 Monitoring Location

According to the EM&A Manual, noise quality monitoring was carried out at the locations as shown in Table 4-3 above. The monitoring locations are illustrated in Appendix D.

4.2.4 Action and Limit Levels

The Action and Limit Levels for the construction noise are shown in Table 4-4 below. In the case of non-compliance of Action and/or Limit level, the Event and Action Plan stipulated in the EM&A Manual shall be implemented.

Time Period	Action	Limit
0700-1900 hours on normal weekdays	When one documented complaint is received	75 dB(A) for residential premises
		70 dB(A) for school and 65 dB(A) during examination period

Table 4-4 Action and Limit Levels for Airborne Construction Noise

4.3 Ground-borne Noise

No ground-borne noise monitoring was conducted in the reporting month since no operation of TBM was carried out.

4.4 Ecological Monitoring

4.4.1 Ecological Monitoring on Avifaunal Communities

Monitoring methodology

In accordance with the Ecological Monitoring Plan, avifaunal communities would be surveyed quantitatively by transect count or/and point count method covering the vicinity of the works area as shown in Table 4-5 below. Birds heard or seen within the survey area would be identified to species level and counted. The nature of construction works within works area conducting during each impact monitoring

would also be recorded. Weather condition and other noticeable activities occurring within or in the vicinity of the survey areas would be recorded. The impact monitoring results would be compared to the baseline data collected before construction. Should any unpredicted indirect ecological impacts arising from the Project be detected, remedial measures would be implemented by the Contractor.

Monitoring location, frequency and duration

In accordance with the EM&A Manual and Ecological Monitoring Plan, ecological monitoring should be conducted at Works Area in MPV, TPP, SSS/ERS, TUW and PHV. With the hoarding erection completed and construction works at MPV, TPP and PHV commenced, ecological monitoring on monthly basis was commenced accordingly. The location, frequency and duration of ecological monitoring at MPV, TPP, SSS/ERS, TUW and PHV are shown in Table 4-5 and figures in Appendix D.

Works Area	**Survey Site**	**Monitoring Location**	**Monitoring Frequency**	**Monitoring Duration**
Mai Po Ventilation Building Works Area (MPV)	MPV-1	• Fishponds in Wetland Conservation Area (WCA) within 500 m from the boundary of MPV works area	Monthly	• During construction phase of MPV works area
Access road leading to TPP	TPP-1/2/3	• The whole alignment of drainage channel KT5 (TPP-1) • The section of drainage channel 95CD along the proposed alignment of access upgrading (TPP-2) • The whole alignment of	Monthly	• During upgrading and operation of access road for construction phase activities

Works Area	Survey Site	Monitoring Location	Monitoring Frequency	Monitoring Duration
		abandoned meander of conservation interest 43CD-1 (TPP-3)		
Access road leading to SSS / ERS	SSS-2a [1]	• The whole alignment of abandoned meanders of conservation interest 95CD-4	Weekly	• During erection of site hoarding
	SSS-3 [1]	• Agricultural land within 500 m from the boundary of SSS/ ERS works area between Shek Kong Road and Kam Sheung Road (SSS-3)	Monthly	• During construction phase of SSS / ERS works area
Tse Uk Tsuen Works Area (TUW)	TUW – 1/2 (TUW-2 grouped with PHV-1 due to overlapping of survey area)	• Agricultural land within 500 m from the boundary of TUW works area to the south of Kam Sheung Road (TUW-1) • Woodland in Conservation Area (CA) within 500 m from the boundary of TUW works area (TUW-2)	Monthly	• During construction phase of TUW works area

Works Area	Survey Site	Monitoring Location	Monitoring Frequency	Monitoring Duration
Pat Heung Ventilation Building Works Area (PHV)	PHV-1 (grouped with TUW-2 due to overlapping of survey area)	• Woodland in CA within 500m from the boundary of PHV works area	Monthly	• During construction phase of PHV works area

Table 4-5 Requirement of Construction Impact Monitoring for Avifaunal Group

Note: 1. Hoarding erection in vicinity of SSS-2a was carried out in April 2011. Construction in vicinity of SSS-1, 2a and 2b has not commenced.

4.4.2 Monitoring of impact at fishpond due to noise/vibrations

In accordance with the Monitoring and Emergency Response Plan, during construction stage, air-borne noise monitoring should be carried out at the respective monitoring location at nearby fishpond (Appendix D) when there are project-related construction activities being undertaken within a radius of 300m from the monitoring location. One set of 30-minute measurement at a frequency of once a week when the above-mentioned construction activities are underway.

As operation of TBM underneath fishponds in Mai Po is not expected in the coming reporting months, no monitoring of ground-borne noise was carried out.

Monitoring of impact due to air-borne noise

Monitoring methodology

With reference to the Monitoring and Emergency Response Plan, the noise acceptance criteria of 75 dB(A) was adopted for the assessment of adverse impact to fisheries due to air-borne noise.

Monitoring location, frequency and duration

The nearest fish-pond located in the vicinity of the works area in Mai Po as shown in Appendix D was identified as a representative air-borne and ground-borne noise/vibration monitoring location.

During construction stage, routine air-borne noise monitoring would be carried out at the respective monitoring location when there are project-related construction activities being undertaken within a radius of 300m from the monitoring station. One set of 30-minute measurement at a frequency of once a week when the above-mentioned construction activities are underway.

Action and Limit Levels

The Action and Limit levels for air-borne noise are defined in the table below. Should non-compliance of the noise quality criteria occur, actions in accordance with the Table 4-6 as should be carried out.

Time Period	Action Level	Limit Level
All time period	When one documented complaint related to adverse impact to fisheries from fish-pond operator or any abnormal ecological monitoring results	75 dB(A) for air-borne noise

Table 4-6: Action and Limit Level for potential impact at fishpond due to air-borne noise

4.5 Landscape and Visual

Monitoring of the implementation of the tree protection measures during construction phase was conducted in accordance with the requirements of EP condition 2.15 (iv). The landscape and visual monitoring and auditing would be conducted once a month throughout the construction stage and covering the entire project site areas.

4.6 Cultural Heritage

4.6.1 Archaeology

No monitoring and reporting is required since construction at Shek Kong Stabling Sidings (SSS) and Lung Kwu Sheng Tan (LKST) have not started.

4.6.2 Built Heritage

No monitoring and reporting is required since construction at ex-Lai Chi Kok

Hospital (LCKH) and SSS have not started.

4.7 Landfill Gas

No monitoring was carried out at Ngau Tam Mei Landfill (NTML) in this reporting month since there was no construction within the (NTML) consultation zone.

Landfill gas monitoring was conducted at Rambler Channel Barging Point which is within the Gin Drinker Bays Landfill (GDBL) consultation zone in the reporting month. Regular landfill gas monitoring was conducted during excavation of about 500mm to 1000mm depth for site formation and wheel washing facility establishment.

Calibrated gas detection equipment, GA 2000 Gas Analyzer was used for detection of Methane, Carbon dioxide and Oxygen gas during excavation works. The frequency of monitoring was once per day if there is excavation works. The measurement was made directly after the excavation has been completed and daily whilst the excavation remains open.

5. MONITORING RESULT

5.1 Air Quality

The monitoring schedule is shown in Appendix E. Results of 24-hour TSP level and the graphical presentation of monitoring results are shown in Appendix F.

In the reporting month, there are exceedances of 24-hr TSP Action Level on 4 April 2011 at AM 3; 29 April 2011 at AM 4; 1 April 2011 at AM 15 and 1 April 2011 at AM17 were recorded in the reporting month. No exceedance of 24-hr TSP Limit Level was recorded in the reporting month. Actions stipulated under the Event and Action Plan (Table 9.4 of the EM&A Manual) were implemented for all exceedances and monitoring frequency was increased.

For the exceedance at AM 3, investigation results revealed that the exceedance might possibly due to construction work at Tai Kong Po Works Area. The 824 Contractor provided additional dust mitigation measures, including covering of stockpile, concreting the temporary slope and improving watering frequency and coverage by automatic sprinklers. The situation would be continuously reviewed by IEC.

For the exceedance at AM 4, investigation results revealed that the exceedance might possibly due to site formation works at northern SSS area. The 823A Contractor was reminded to enhance the dust suppression measure including covering of stockpile and regular watering on haul road. The situation would be continuously reviewed by IEC.

For the exceedance at AM 15, investigation results revealed that the exceedance might possibly due to construction works near Lin Cheung Road Works Area. The 803A Contractor was reminded to enhance the dust suppression measure including covering of stockpile and regular watering on haul road. The situation would be continuously reviewed by IEC.

For exceedance at AM 17, investigation results revealed that the exceedance might possibly due to the traffic movement at the temporary material storage area opposite to Austin Road West. The 810B Contractor was reminded to watering the unpaved area more frequently. The situation would be continuously reviewed by IEC.

5.2 Noise

The monitoring schedule is shown in Appendix E. Results of measured noise level, in terms of $L_{eq(30min)}$ and graphical presentations are presented in Appendix F.

In the reporting month, noise exceedances of air-borne noise Limit Level were recorded at Kong Tai Road Village House (CN 5) on 21 April 2011; HKIVE Haking Wong Waterfront Annex (CN 23) on 6, 13 and 27 April 2011 (exceedance on 20 April was considered invalid as there was no school day); St. Mary's Church Mok Hing Yiu College (CN 25) on 7 April 2011; The Waterfront (CN 32) on 6, 20 and 29 April 2011 and The Arch (CN 33) on 7 April 2011.

For the noise exceedance at CN 5, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. Upon investigation, the exceedance might possible be due to construction works by 824 Contractor. The Contractor was reminded to provide noise mitigation measures to minimize the noise impact.

Regarding the noise exceedances at CN 23, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. The noise exceedance recorded on 6 and 27 April 2011 were caused by 805 site works, while the exceedance recorded on 13 April 2011 was mainly caused by other non-project sources. The Contractor implemented mitigation measures to minimize the noise impact.

Regarding noise exceedance recorded at St. Mary's Mok Hiu Hing College (CN 25), actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. It was found that pile removal work at Nam Cheong Launching Shaft near CN 25 by Contractor 820 might have caused the noise exceedance. The Contractor was reminded to enhance the noise mitigation measures to minimize noise nuisance to

the nearby NSRs.

For the noise exceedances at The Waterfront (CN 32) and The Arch (CN 33) in West Kowloon, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractors were informed of the exceedances. The investigation result revealed that noise source may possibly due to works by 803A, 803B, 803D and 810B Contractors. Additional noise mitigation measures proposed by the Contractor were reviewed by IEC and ET and implemented by the 803A, 803B, 803D and 810B Contractors to minimize the noise impact. All contractors in WKT works area were reminded to enhance the noise mitigation measures to comply with the statutory requirement and minimize noise nuisance to the nearby NSRs.

In addition, there were two noise exceedances of Action Level triggered due to noise complaint during daytime hours received in the reporting month. Please refer to Section 7 for details of complaint.

5.3 Ecological Monitoring

5.3.1 Ecological Monitoring on Avifaunal Communities

Ecological monitoring at MPV

Monthly avifauna monitoring at MPV work site was conducted on 12 April 2011. The weather conditions and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring were summarized in Table 5-1. The MPV-1 survey site comprised about 20 fishponds with most of them being actively managed (Figure C8016/C/XRL/ENS/M51/001 in Appendix D refers). Commonly observed pond management activities during the monitoring include pond aeration, removal of bund weeds and fish feeding. Ongoing construction activities were also recorded at the works area of the project "Proposed Comprehensive Development at Wo Shang Wai, Yuen Long" (hereinafter to be referred to as "Wo Shang Wai Project") located near Point Count Location MPV-1/P9. The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date	Weather Conditions	Noticeable Activities in the MPV-1 Survey Site
12 April 2011	Sunny, windy	• Pond aeration • Feeding of fish

Table 5-1 Weather condition and noticeable activities observed in the MPV-1 survey site during monitoring in April 2011

A total of 273 individuals from 36 avifauna species were recorded from the Point Count Locations at MPV-1 in April 2011 (Table 5-2 refers). The total number of species recorded during the monitoring was 41. The population of the avifauna recorded mainly consisted of Scaly-breasted Munia, Barn Swallow, ardeids (e.g. egrets and herons), wagtails (e.g. Yellow Wagtail and White Wagtail), Common Sandpiper and other widespread resident species (e.g. Plain Prinia, Yellow-bellied Prinia, Spotted Dove and Eurasian Tree Sparrow). Other recorded waterbirds and wetland-dependent species include Little Grebe, Black-headed Gull, Common Kingfisher, Pied Kingfisher, White-throated Kingfisher, Osprey and Collared Crow. Detailed records of avifauna at MPV-1 survey site are presented in Appendix G.

The monitoring results of April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of species and abundance recorded in April remains higher than that of the baseline.

The monitoring results indicated the fishponds within the survey area were utilized by a large number of waterbirds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey	MPV-1	
	No. of Species	Abundance
12 April 2011	36	273
August to October 2009 [1] (Source: monthly averaged number obtained	24	230

in Baseline Bird Survey)		

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-2 Number of species and abundance of avifauna recorded in April 2011 during bird survey at the point count locations of the MPV-1 survey site

Month	**Total Number of Species Recorded [1,2]**
12 April 2011	41 (9)
August to October 2009 [3] (Source: monthly averaged number obtained in Baseline Bird Survey)	24 (5)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-3 Total number of avifauna species recorded during bird survey at the MPV-1 survey site

Ecological monitoring at Tai Kong Po (TPP-1)

The avifauna monitoring location for the proposed works area of the TPP access road was sub-divided into three survey sites namely TPP-1, TPP-2 and TPP-3. The TPP-1 survey site is a drainage channel (KT5) with gabion / masonry banks at upper portion. The rest of the channel is trapezoidal with vegetated grasscrete banks on both sides of the channel. The downstream end of the channel joins up with a main drainage channel (95CD) (Figure C8016/C/XRL/ENS/M51/003 in Appendix D refers).

The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-4. The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	Weather Condition	Noticeable Activities Observed in the TPP-1 Survey Site
12 April 2011	Overcast, windy	• Construction works within the proposed access road near Point Count Location TPP-1/P1

Table 5-4 Weather Condition and Noticeable Activities Observed in the TPP-1 Survey Site during the Monitoring in April 2011

A total of 235 individuals from 30 avifauna species were recorded from the Point Count Locations at TPP-1 in April 2011 (Table 5-5 refers). The total number of species recorded during the monitoring was 31. The population of the avifauna recorded mainly consisted of Sandpipers (e.g. Wood Sandpiper and Green Sandpiper), Barn Swallow and residents (e.g. Spotted Dove, Red-whiskered Bulbul, Yellow-bellied Prinia, Scaly-breasted Munia and Black-collared Starling). Other recorded waterbirds include ardeids (e.g. Little Egret, Cattle Egret and Chinese Pond Heron), White-breasted Waterhen and Common Snipe. It is typical in most lowland streams of Hong Kong (polluted and/or channelized at their lower courses) that lowland wetland bird species such as Chinese Pond Heron, White-breasted Waterhen, Common Kingfisher and Grey Wagtail could be found in low densities (Wong *et al*., 2009). Bird activity in channelized streams is largely restricted to exploiting food resources, typically fish or insects (Wong *et al*., 2009). Detailed records of avifauna at TPP-1 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline bird survey conducted from August to October 2009. The number of bird species and abundance of bird species are higher than that of baseline results. This is explained by the presence of winter visitors such as Common Snipe, Olive-backed Pipit, Red-throated Pipit, White-shouldered Starling and Japanese White-eye. As April is a transitioning month into the wet season, so it is probable to see winter visitors who have not departed.

The monitoring results indicated the drainage channel within the survey area was utilized by waterbirds and water-dependent species in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the

Project were identified.

Survey Period	TPP-1 Survey Site	
	No. of Bird Species	Abundance of Bird Species
12 April 2011	30	235
August to October 2009 [1]	15	174

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-5 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the TPP-1 Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
12 April 2011	31 (4)
August to October 2009 [3]	15 (4)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-6 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the TPP-1 Survey Site

Ecological monitoring at Tai Kong Po (TPP-2)

The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-7. The TPP-2 survey site covered a section of main drainage channel 95CD, which is a concrete trapezoidal channel with grasscrete banks. Plantation of native or landscape vegetation was observed along the embankment of the channel (Figure C8016/C/XRL/ENS/M51/002 in Appendix D refers). The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	Weather Condition	Noticeable Activities Observed in the TPP-2 Survey Site
12 April 2011	Overcast, windy	• No project-related construction activities located in the vicinity

Table 5-7 Weather Condition and Noticeable Activities Observed in the TPP-2 Survey Site during the Monitoring in April 2011

A total of 48 individuals from 16 avifauna species were recorded from the Point Count Locations at TPP-2 in April 2011 (Table 5-8 refers). The total number of species recorded during the monitoring was 21. The population of the avifauna recorded mainly consisted of Barn Swallow and residents (e.g. Spotted Dove, Japanese White-eye and Eurasian Tree Sparrow). Other recorded waterbirds included Little Egret, Little Ringed Plover and sandpipers (e.g. Green Sandpiper,

Wood Sandpiper and Common Sandpiper). It is typical in most lowland streams of Hong Kong (polluted and/or channelized at their lower courses) that lowland wetland bird species such as Chinese Pond Heron, White-breasted Waterhen, Common Kingfisher and Grey Wagtail could be found in low densities (Wong *et al*., 2009). Detailed records of avifauna at TPP-2 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of bird species recorded from the Point Count Locations of TPP-2, and the total number of species and species of conservation interest recorded from TPP-2 survey site in April 2011 were of similar magnitude as the baseline results (Table 5-8 and Table 5-9 refer).

The monitoring results indicated the main drainage channel within the survey area was utilized by typical lowland stream birds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	**TPP-2 Survey Site**	
	No. of Bird Species	**Abundance of Bird Species**
12 April 2011	16	48
August to October 2009 [1]	14	66

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-8 Number of Bird Species and Abundance of Bird Species Recorded in April 2011. Avifauna Monitoring at the Point Count Locations of the TPP-2 Survey Site

Survey Period	**Total Number of Bird Species Recorded [1,2]**
12 April 2011	21 (2)
August to October 2009 [3]	16 (3)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-9 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the TPP-2 Survey Site

Ecological monitoring at Tai Kong Po (TPP-3)

The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-10. The TPP-3 survey site is an abandoned meander (43CD-1) of conservation interest with natural banks and substratum. The earthen banks of the meander were mostly dominated by grasses and weeds. The section near point count location TPP-3/P1 was found to be usually wet though the water was quite stagnant. Due to its close proximity to a village access road of Kam Hing Wai and Shui Mei Tsuen, this section of meander was subject to higher disturbance from villagers and traffic. Point count locations TPP-3/P2 and TPP-3/P3 were only seasonally wet (Figure C8016/C/XRL/ENS/M51/002 in Appendix D refers). The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	**Weather Condition**	**Noticeable Activities Observed in the TPP-3 Survey Site**
12 April 2011	Overcast, windy	• No project-related construction activities located in the vicinity

Table 5-10 Weather Condition and Noticeable Activities Observed in the TPP-3 Survey Site during the Monitoring in April 2011

A total of 25 individuals from 7 avifauna species were recorded from the Point Count Locations at TPP-3 in April 2011 (Table 5-11 refers). The total number of species recorded during the monitoring was 7. The population of the avifauna recorded consisted of widespread resident species (e.g. Red-whiskered Bulbul, Chinese Bulbul, Masked Laughingthrush and Yellow-bellied Prinia), and summer visitor Black Drongo. It is typical in most lowland streams of Hong Kong (polluted and/or channelized at their lower courses) that lowland wetland bird species such as Chinese Pond Heron, White-breasted Waterhen, Common Kingfisher and Grey Wagtail could be found in low densities (Wong *et al*., 2009). Detailed records of avifauna at TPP-3 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of bird species and abundance recorded from the Point Count Locations of TPP-3, and the total number of species and species of conservation interest recorded from TPP-3 survey site in April 2011 were higher than the baseline results (Table 5-11 and Table 5-12 refer). Survey records in April 2011 demonstrate an increase in abundance of the overall common resident species recorded such as Red-whiskered Bulbul, Masked Laughingthrush and Yellow-bellied Prinia.

The monitoring results indicated the abandoned meander within the survey area was utilized by typical lowland stream birds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	TPP-3 Survey Site	
	No. of Bird Species	Abundance of Bird Species
12 April 2011	7	25
August to October 2009 [1]	4	7

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-11 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the TPP-3 Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
12 April 2011	7 (0)
August to October 2009 [3]	3 (1)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-12 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the TPP-3

Survey Site

Ecological monitoring at Shek Kong Stabling Sidings (SSS-2a)

Weekly avifauna monitoring at SSS-2a was conducted during the period of hoarding erection on 12 April 2011. Monthly monitoring at SSS-2a would be commenced subject to construction programme. Hoarding erection and construction in the vicinity of SSS-1/2b was yet commenced and ecological monitoring would be conducted according to the construction programme. SSS-2a survey site is an abandoned meander (95CD-4) of conservation interest located in the north of Wan Toi Shan. The meander is adjacent to car repairing workshops and garage. Riparian vegetation was well established although some areas of the banks were lined with concrete. The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-13

Date of Monitoring	**Weather Condition**	**Noticeable Activities Observed in the SSS-2a Survey Site**
12 April 2011	Overcast	• Hoarding erection in the vicinity of Point Count Location SSS-2a/P1

Table 5-13 Weather Condition and Noticeable Activities Observed in the SSS-2a Survey Site during the Monitoring in April 2011

A total of 16 individuals from 9 avifauna species were recorded from the Point Count Locations at SSS-2a in April 2011 (Table 5-14 refers). The total number of species recorded during the monitoring was 9. The population of the avifauna recorded consisted mainly of widespread resident species (e.g. Red-whiskered Bulbul, Chinese Bulbul and Eurasian Tree Sparrow). Detailed records of avifauna at SSS-2a are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of bird species and abundance recorded from the Point Count Locations of SSS-2a, and the total number of species and species of conservation interest recorded from SSS-2a survey site in April 2011 were of similar magnitude as the baseline results (Table 5-14 and Table 5-15 refer).

The monitoring results indicated the abandoned meander within the survey area was utilized by typical lowland stream birds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	SSS-2a Survey Site	
	No. of Bird Species	Abundance of Bird Species
12 April 2011	9	16
August to October 2009 [1]	6	15

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-14 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the SSS-2a Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
12 April 2011	9 (0)
August to October 2009 [3]	6 (1)

Note:

1. Total number of bird species recorded included the avifauna recorded from point count locations only as there is no walk transect for SSS-2a survey site.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-15 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the SSS-2a Survey Site

Ecological monitoring at Shek Kong Stabling Sidings (SSS-3)

Monthly avifauna monitoring at SSS-3 work site was conducted on 19 April 2011 during the construction of SSS / ERS. Construction in the vicinity of SSS-1/2b was yet commenced and ecological monitoring would be conducted according to the construction programme. The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-16. The farmland in SSS-3 survey site displayed a distinctive seasonal crop rotation pattern between wet agriculture (*Ipomoea aquatica*) in summer season and dry agriculture (seasonal flowers such as *Gladiolus*

gandavensis) in winter season (Figure C8016/C/XRL/ENS/M51/004 in Appendix D refers). The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	**Weather Condition**	**Noticeable Activities Observed in the SSS-3 Survey Site**
19 April 2011	Sunny	- Site office formation at Point Count Location SSS-3/P5 -Mainly dry agricultural activities were observed such as farming of vegetables and ornamental flowers

Table 5-16 Weather Condition and Noticeable Activities Observed in the SSS-3 Survey Site during the Monitoring in April 2011

A total of 208 individuals from 31 avifauna species were recorded from the Point Count Locations at SSS-3 in April 2011 (Table 5-17 refers). The total number of species recorded during the monitoring was 37. The population of the avifauna recorded mainly consisted of resident species (e.g. Spotted Dove, Barn Swallow, Red-whiskered Bulbul, Yellow-bellied Prinia, Eurasian Tree Sparrow and Crested Myna) and ardeids (e.g. Cattle Egret and Chinese Pond Heron). It was found that the dominant species present in dry farmland included resident such as Spotted Dove, Barn Swallow, Eurasian Tree Sparrow, Black-collared Starling and Crested Myna. Meanwhile, the ornamental flower such as peach blossom is attractive to some species such as Common Blackbird, Olive-backed Pipit, Japanese White-eye and Yellow-browed Warbler (Wong *et al.*, 2009). Detailed records of avifauna at SSS-3 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of bird species recorded from the Point Count Locations of SSS-3 and the total number of species and species of conservation interest recorded from SSS-3 survey site in April 2011 were of similar magnitude as the baseline results.

The monitoring results indicated the agricultural lands within the survey area were utilized by typical bird species found in dry farmland in April 2011 during the

monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	SSS-3 Survey Site	
	No. of Bird Species	Abundance of Bird Species
19 April 2011	31	208
August to October 2009 [1]	24	188

Note:

1. Monthly average obtained from baseline bird survey.

Table 5-17 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the SSS-3 Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
19 April 2011	34 (1)
August to October 2009 [3]	24 (3)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-18 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the SSS-3 Survey Site

Ecological monitoring at PHV and TUW

Monthly avifauna monitoring at TUW-1 work site was conducted on 19 April 2011 during the construction of TUW. The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-19. The TUW-1 survey site encompassed a large piece of agricultural land located to the south of Kam Sheung Road (i.e. Tse Uk Tsuen). The agricultural land in TUW-1 survey site shared the habitat characteristics of SSS-3 survey site. Similar seasonal alternation between wet and dry agriculture was also recorded from TUW-1 survey site (Figure C8016/C/XRL/ENS/M51/005 in Appendix D refers). The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	Weather Condition	Noticeable Activities Observed in the TUW-1 Survey Site
19 April 2011	Sunny	• Site investigation works near Point Count Location TUW-1/P4. • Mainly dry agricultural activities were observed such as farming of vegetables and ornamental flowers

Table 5-19 Weather Condition and Noticeable Activities Observed in the TUW-1 Survey Site during the Monitoring in April 2011

A total of 205 individuals from 26 avifauna species were recorded from the Point Count Locations at TUW-1 in April 2011 (Table 5-20 refers). The total number of species recorded during the monitoring was 29. The population of the avifauna recorded mainly consisted of residents (e.g. Spotted Dove, Barn Swallow, Red-whiskered Bulbul, Yellow-bellied Prinia and Eurasian Tree Sparrow). Other recorded waterbirds and wetland-dependent species included Cattle Egret, Chinese Pond Heron and Black Kite. It was found that the dominant species present in dry farmland included resident insectivores such as Crested Myna, Spotted Dove, Barn Swallow, Eurasian Tree Sparrow and Black-collared Starling. Meanwhile, the ornamental flowers such as gladioli and peach blossom are attractive to some species such as Common Blackbird, Olive-backed Pipit, Japanese White-eye and Yellow-browed Warbler (Wong *et al*., 2009). Detailed records of avifauna at TUW-1 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season data from August to October 2009. The number of bird species and abundance recorded from the Point Count Locations of TUW-1, and the total number of species of conservation interest recorded from TUW-1 survey site in April 2011 were higher than the baseline results (Table 5-20 and Table 5-21 refer). The increase in abundance in April 2011 was mainly composed of abundant resident species such as Red-whiskered Bulbul, Barn Swallow and Eurasian Tree Sparrow recorded during monitoring.

The monitoring results indicated the agricultural lands within the survey area were utilized by typical bird species found in dry farmland in April 2011 during the

monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	TUW-1 Survey Site	
	No. of Bird Species	Abundance of Bird Species
19 April 2011	26	205
August to October 2009 [1]	22	130

Note:
1. Monthly average obtained from baseline bird survey.

Table 5-20 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the TUW-1 Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
19 April 2011	29 (1)
August to October 2009 [3]	22 (3)

Note:

1. Total number of species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-21 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the TUW-1 Survey Site

Since the extent of PHV-1 survey site is overlapped with that of TUW-2 survey site, the survey data of the TUW-2 and PHV-1 survey sites were reported collectively. Monthly avifauna monitoring at TUW-2 and PHV-1 survey site was conducted on 19 April 2011 during the construction of TUW and PHV. The weather condition and other noticeable activities occurring within or in the vicinity of the survey area during the monitoring are summarized in Table 5-22. The TUW-2 and PHV-1 survey site comprised the woodland in Conservation Area (CA) within 500 m from the boundary of the PHV works area (Figure C8016/C/XRL/ENS/M51/006 in Appendix D refers). The bird species and their abundance recorded during the avifauna monitoring for the reporting month are presented in Appendix G.

Date of Monitoring	Weather Condition	Noticeable Activities Observed in the TUW-2 and PHV-1 Survey Site
19 April 2011	Sunny	• No project-related construction activities located in the vicinity

Table 5-22 Weather Condition and Noticeable Activities Observed in the TUW-2 and PHV-1 Survey Site during the Monitoring in April 2011

A total of 19 individuals from 10 avifauna species were recorded from the Point Count Locations at TUW-2 and PHV-1 in April 2011 (Table 5-23 refers). The total number of species recorded during the monitoring was 20. The population of the avifauna recorded consisted largely of residents (e.g. Red-whiskered Bulbul, Chinese Bulbul and Japanese White-eye). It is typical that the forest bird community in Hong Kong is dominated by a few habitat-generalist species, including Chinese Bulbul, Red-whiskered Bulbul, Common Tailorbird and Japanese White-eye (Wong *et al.*, 2009). Other recorded species included common residents such as Scarlet Minivet, Scarlet-backed Flowerpecker and Streak-breasted Scimitar Babbler. A species of conservation interest, Rufous-capped Babbler was recorded. Detailed records of avifauna at TUW-2 and PHV-1 are presented in Appendix G.

The monitoring results in April 2011 were compared against the wet season results of the baseline data from August to October 2009. The number of bird species and abundance recorded from the Point Count Locations of TUW-2 and PHV-1, and the total number of species and species of conservation interest recorded from TUW-2 and PHV-1 survey site in April 2011 were of similar magnitude as the baseline results (Table 5-23 and Table 5-24 refer).

The monitoring results indicated the woodland within the survey area was utilized by typical forest birds in April 2011 during the monitoring. No significant fluctuation in the number of species and abundance of avifauna was observed. Therefore, no adverse indirect impacts arising from the Project were identified.

Survey Period	TUW-2 and PHV-1 Survey Site	
	No. of Bird Species	Abundance of Bird Species
19 April 2011	10	19
August to October 2009 [1]	7	14

Note:
1. Monthly average obtained from baseline bird survey.

Table 5-23 Number of Bird Species and Abundance of Bird Species Recorded in April 2011 Avifauna Monitoring at the Point Count Locations of the TUW-2 and PHV-1 Survey Site

Survey Period	Total Number of Bird Species Recorded [1,2]
19 April 2011	20 (1)
August to October 2009 [3]	10 (0)

Note:

1. Total number of bird species recorded included the avifauna recorded from both point count locations and walk transect.

2. The numbers in brackets denote the number of species of conservation interest.

3. Monthly average obtained from baseline bird survey.

Table 5-24 Total Number of Bird Species Recorded in April 2011 Avifauna Monitoring at the TUW-2 and PHV-1 Survey Site

5.3.2 Monitoring of impact at fishpond due to noise

In accordance with the Monitoring and Emergency Response Plan, impact noise monitoring was conducted at fish pond on weekly basis for assessment of impact at fishponds due to noise. The results are displayed in the table below. It was revealed from the monitoring results that all monitoring results were within the Limit Level of 75 dB(A). Based on the monitoring results, there was no adverse impact at fishpond due to noise.

Monitoring Date	L_{eq}, dB(A)
9/4/2011	54
12/4/2011	60
19/4/2011	54

Monitoring Date	L_{eq}, dB(A)
26/4/2011	47

Table 5-25 Noise monitoring results at fishpond in Mai Po

5.4 Waste Management

The quantities of waste disposed from this Project during the reporting month and the previous 2 months are summarized in the following table:

Reporting Month	Inert C&D [1]Materials (tonnes)	Non-inert C&D [2]Materials (tonnes)	Chemical Waste (Litre)
Contract 802			
February 2011	0	0	0
March 2011	1146.0	4.8	0
April 2011	483.4	1.1	0
Contract 803A			
February 2011	10271.9	23.9	0
March 2011	18889.4	28.6	2000
April 2011	6537.1	14.9	0
Contract 803B			
February 2011	5302.3	5.4	0
March 2011	7049.2	16.3	0
April 2011	2826.0	6.0	0
Contract 803D			
February 2011	2186.6	2.4	1000
March 2011	4054.4	12.0	800
April 2011	1676.7	0	0
Contract 805			
February 2011	475.9	0	0
March 2011	221.8	5.3	
April 2011	791.5	0	
Contract 810B			
February 2011	0	0	0
March 2011	14521.0	0.2	0

Reporting Month	**Inert C&D [1]Materials (tonnes)**	**Non-inert C&D [2]Materials (tonnes)**	**Chemical Waste (Litre)**
April 2011	116023.0	15.3	0
Contract 811A			
February 2011	7598.9	19.5	0
March 2011	8996.5	29.4	0
April 2011	9379.9	16.9	200
Contract 811B			
February 2011	12721.1	44.0	0
March 2011	20013.4	43.8	0
April 2011	16778.0	30.0	1400
Contract 820			
February 2011	6520.2	21.1	0
March 2011	10501.6	31.9	0
April 2011	9062.8	11.8	0
Contract 821			
February 2011	1410.0	3.0	0
March 2011	19498.5	4.8	0
April 2011	18168.5	3.1	0
Contract 822			
February 2011	16968.1	13.8	0
March 2011	30841.8	16.7	0
April 2011	29281.1	22.5	0
Contract 823A			
February 2011	345.3	39.8	0
March 2011	2497.6	93.8	0
April 2011	3031.5	99.3	0
Contract 823B			
February 2011	0	28.8	0
March 2011	33447.2	519.1	0
April 2011	85863.5	451.4	0
Contract 824			
February 2011	1252.0	394.0	0
March 2011	3102.0	537.5	0
April 2011	116.0	203.0	0
Contract 825			

Reporting Month	**Inert C&D [1]Materials (tonnes)**	**Non-inert C&D [2]Materials (tonnes)**	**Chemical Waste (Litre)**
February 2011	5181.1	7.0	0
March 2011	14021.9	0	0
April 2011	34538.0	12.9	0

Table 5-26 Summary of construction waste generated and disposed

Note:

1. Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.

2. Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse.

3. Asbestos waste is not shown.

4. Alternative disposal sites for inert C&D Material from Contract 821 include Pak Sha Tau Quarry, Zhuhai, China.

5. Alternative disposal sites for inert C&D Material from Contract 822 include Lam Tei Quarry and WENT landfill

6. Alternative disposal sites for inert C&D Material from Contract 825 include Ha Ko Po Tsuen Residential Development, Fan Kam Road Ku Tung South Residential Development and Sludge Treatment Facility in Tuen Mun.

5.5. Landscape and Visual

5.5.1 Monitoring Requirement

A Certified Arborist was employed and has conducted inspection and audits and found that the tree protection works being carried out by the civil works and transplanting contractors were in accordance with EP/EIA.

Monitoring of the implementation of the tree protection measures during construction phase was conducted in accordance with the requirements of EP condition 2.15 (iv).

The landscape and visual monitoring and auditing will be conducted on regular basis throughout the construction stage and covering the entire project site areas.

5.5.2 Audit Result

Monthly monitoring and audit was undertaken in accordance with the requirement of EP condition 2.15 (iv)

Tree Transplanting Works at Contract 801

Root ball preparation / wrapping for transplanted trees were recommended to be improved. Pesticide treatment was applied to the palms tree in temporary holding nursery (Siu Lang Shui). Some improvement from previous month was observed but the health condition of trees needs further improvement. Fertiliser application was considered to be required. Watering frequency needs to be adjusted.

Tree Protection Work 802

Retained tree within construction was under monitoring and checked. However, construction activities were found close to tree canopy. The contractor was reminded on tree protection.

Tree Protection Work 803A

Trees to be retained have been identified and protected with fencing. Tree protection zone should be properly established with solid protective fencing.

Tree Protection Work 805

Areas underneath retained trees were observed to be used as car parking space. Protective measure should be improved. T8986 have symptom of bark peeling and suffer from canker disease.

Tree Protection Work 811A

Protective fencing was recommended to be improved which was found to be close to the trees. Light weight equipment and materials still stored insides Tree Protection Area. This storage materials are recommended to be removed.

Tree Protection Work 811B

Construction materials are stored within the tree protection area. Protective measures of retained tree should be reinforced to ensure the tree are properly protected. Contractor was requested to be cautious when operating machineries near protection zone.

Tree Protection Work 820

Site hoarding and car park surfacing formed around retained trees. Padding is required to be applied for better tree protection.

Tree Protection Work 821

Some of the trees in contract 821 with extensive decay in trunk and main stem. Contractor is required to apply for tree remove or provide physical support.

Tree Protection Work 822

The overall tree protection measures is required to be further improved. The contractor is required to follow the recommendations given by EP Arborist for the improvement of tree protection. Remedial action by contractor for potential hazardous tree for T7060 was requested.

Tree Protection Work 823A

Tree protection work was commenced. Measures in protecting tree on site should be further improvement.

Tree Protection Work 824

Protective fencing around retained trees was observed insufficient and should be improved. Storage of heavy construction materials within tree protection zone was found. Mitigation action is required to be implemented.

Tree Transplanting Work 826

Trees have been transplanted to area near new site office. The condition of transplanted trees was satisfactory.

5.6. Landfill Gas

No monitoring was carried out at Ngau Tam Mei Landfill (NTML) in this reporting month since there was no construction within the (NTML) consultation zone.

Regular landfill gas monitoring was conducted by the Contractor during excavation of about 500mm to 1000mm depth for site formation and wheel washing facility construction at Rambler Channel Barging Point. The monitoring results show no exceedance of relevant safety limit. Details of the monitoring results and monitoring location plan are attached in Appendix J.

6. SITE INSPECTION

Regular site inspections attended by representatives from ET and Contractors were carried out at 802/805 in Nam Cheong, 803A, B, D, 810B and 811A/B in West Kowloon, 820/821 in Nam Cheong, 822 in Shing Mun, Shek Yam and So Kwun Wat, Tsing Chau Tsai and Tai Shu Ha Road West, 823A/B in Shek Kong Stabling Sidings, 824 in Tai Kong Po and Ngau Tam Mei, 825 in Mai Po and Siu Lam Barging Point and dates are shown in the following table. In addition to the regular site inspections attended by ET and Contractors, monthly IEC environmental audits attended by IEC, ET and Contractors were held on 13 April 2011 in 802; 6 April 2011 in 803A; 12 April 2011 in 803B; 6 April 2011 in 803D; 20 April 2011 in 810B; 13 April 2011 in 805; 12 April 2011 in 811A; 11 April 2011 in 811B; 28 April 2011 in 820; 28 April 2011 in 821, 11 April 2011 in 822; 6 April 2011 in 823A; 4 April 2011 in 823B; 19 April in 824 and 26 April 2011 in 825.

Contract	**Date of Site Inspections**
802	8/4 13/4, 20/4 and 27/4
803A	6/4, 13/4, 20/4, and 27/4
803B	1/4, 12/4, 21/4 and 29/4
803D	6/4, 13/4, 20/4, and 27/4
810B	6/4, 13/4, 20/4, and 27/4
805	6/4, 11/4, 21/4 and 27/4
811A	12/4, 19/4 and 26/4
811B	6/4, 11/4, 19/4 and 16/4
820	7/4, 14/4, 21/4 and 28/4
821	7/4, 12/4, 19/4 and 28/4
822	4/4, 11/4, 18/04 and 29/4
823A	1/4, 6/4, 13/4, 21/4 and 27/4

Contract	Date of Site Inspections
823B	4/4, 12/4, 20/4 and 26/4
824	8/4, 12/4, 19/4 and 26/4
825	4/4, 11/4, 18/4 and 26/4

Table 6-1: Date of site inspection

All observations have been recorded in the audit checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary. The key observations from these site inspections and Contractor's follow-up action are summarized in Table 6-2 below. No non-compliance was observed.

Item	Description	Contractor's Follow-up Action(s) Undertaken
Contract 802		
1	The oil drums and buckets were not provided with leakage container.	The oil drums and buckets were not provided with leakage container. The buckets of lubricant oil were placed inside the drip tray.
2	Main haul road near site office was dry.	Water spraying was provided frequently.
3	Chemical spillage was found near the power-pack at Zone 3.	The chemical spillage was removed and collected in chemical waste storage area. The sub-contractor was reminded to provide sheeting to prevent soil contamination.
Contract 803A		

Item	Description	Contractor's Follow-up Action(s) Undertaken
1	It was observed that there was no proper noise mitigation measures provided for the machines, including air compressor, drilling machine and generator when working at works area opposite to the residential premises at Lin Cheung Road.	Noise barrier or proper noise mitigation measures were provided for the machines when in operation.
2	It was observed that the sedimentation tanks at the wastewater treatment plant were full of sediment and water overflew.	The sedimentation tanks have been cleared and the nominated person will closely monitor the plant to avoid overflow.
3	It was observed that some oil drums were placed on bare ground.	Drip tray was provided to the drums when kept on site.
Contract 803B		
1	It was observed that dark smoke was emitted from the exhaust of air compressor placed on-site.	The Contractor was arranged maintenance to the machine.
2	It was observed that the stockpile was not properly covered when not in use.	More frequent to water the stockpile.
3	It was observed that empty chemical bottles were not stacked at the wastewater treatment plant without proper storage.	All the used chemical bottles have been placed at the designated area on site.
Contract 803D		
1	It was observed that over 20 nos. of cement bags were not properly stored on site near the works areas opposite to Elements	Proper cover the cement bags with the tarpaulin when stored on site and not in use.
2	It was observed that greasy water at the drip tray of chemical store on-site.	The greasy water was cleared up properly.

Item	Description	Contractor's Follow-up Action(s) Undertaken
Contract 805		
1	The wastewater treatment and drainage system was not properly implemented.	All wastewater has been diverted to the sedimentation tank for treatment before discharging into storm drain.
2	Dust suppression measure was not implemented.	Dust suppression measure was provided
3	Environmental mitigation measure (for both noise and dust) was not provided for the slab breaking work.	All mitigation measure has been provided for the slab breaking.
Contract 810B		
1	It was observed that crack on bund against surface runoff along the seashore.	The Contractor repaired it at once after the finding made.
2	It was observed that the protection along the sea edge was not sufficient to avoid muddy water flew into the sea at the barging area.	Sufficient sandbags were placed along the sea edge to prevent muddy water enter into the sea.
3	It was observed that the condition of protective cover for Type 3 marine sediment storage tanks was not good.	The Contractor covered the tanks properly to minimize the water entering potentially and enhance the regular checks accordingly.
Contract 811A		
1	Haul road on site was dry and dusty	Watering frequency was increased
2	Chemicals were found not properly stored on site	Chemical were stored properly with drip trays provided underneath
3	Stockpiling of excavated materials was found on site without proper covering	Provided impervious sheet for the stockpiling materials
Contract 811B		

Item	Description	Contractor's Follow-up Action(s) Undertaken
1	Stockpiling of excavated materials was found on site without proper covering	Provided impervious sheet for the stockpiling materials
2	Haul road on site was dry and dusty	Watering frequency was increased
3	Noise mitigation measures were not provided for some of noisy plants (i.e. breakers, etc).	Noise absorbing materials were provided for the plants.
Contract 820		
1	Stacking of pipe was observed underneath the retained trees near D-wall Box A at Launching Shaft works area.	The pipes were removed from the retained trees.
2	Dry soil surface and exposed slope were observed at NC1.	Regular water was provided to the exposed surface.
3	Soil and debris near gully was observed in Rising Main works area.	Soil and debris near gully was cleared and sand bag bund was constructed to surround the gully.
Contract 821		
1	Bared ground at the NC Barging Point was not paved or covered which may lead to muddy water discharge into sea.	Cement spraying on the exposed surface was provided.
2	Oil stain was observed under plants at KCV works area.	Drip tray was provided during maintenance of plant.
3	A gap at the hoarding at KCV works area near Weathly Industrial Building was obverted.	The gap was blocked.
Contract 822		

Item	Description	Contractor's Follow-up Action(s) Undertaken
1	Dust suppression was not implemented for the rock breaking work at Pat Heung.	Water spraying is being provided and the workers were reminded of the dust mitigation requirement.
2	Mud and leaves were accumulated along the surface drain at Pet Heung.	The mud and leaves have been cleared from the u-channel. Weekly clearing is carried out.
3	Chemicals were not provided with any leakage container at Pet Heung.	Drip tray has been provided. The subcontractor was reminded of the chemical storage requirement.
Contract 823A		
1	Slope at Nam Hing West Road Works Area should be protected to minimize generation of muddy water	Slope was properly protected by covering.
2	Mud was found deposited at U-channel in Tsat Sing Kong Area	Mud was cleared to avoid overflow in case of rain
Contract 823B		
1	Muddy water generated from wheel washing was found outside the site entrance of Tsat Sing Kong.	Muddy water was cleared and the method and arrangement of wheel washing was improved.
2	Regular watering on main haul road was observed. However, no watering was provided on the haul road near the site formation/excavation area in works area 4.20A, 4.20B and 4.20C.	Water browser and manual water sparing on haul road and stockpile of material was provided.
3	Insufficient protection/ preventative measures were provided to the exposed surface nearby water bodies in works area 4.8, 4.19D, 4.19E and 4.23F.	Exposed slope was covered by tarpaulin sheet.

Item	Description	Contractor's Follow-up Action(s) Undertaken
Contract 824		
1	Ground surface at Ngau Tam Mei site was dry and dusty	Watering frequency was improved for dust suppression
2	Covering for cement mixing area at the Tai Kong Po site should be improved	Proper covering was provided for dust suppression
3	Oil stain was observed at Ngau Tam Mei site	Source of stain was identified with leaked oil removed and treated as chemical waste
Contract 825		
1	Covering for the cement mixing area should be improved	Proper covering was provided for dust suppression

Table 6-2 Summary of site inspections, recommendations and follow-up actions

7. NON-COMPLIANCE AND DEFICIENCY

7.1 Summary of Complaint

For this reporting month, a total of 5 environmental complaints were referred from EPD. There are a total of 47 environmental complaints since commencement of the construction. The complaints were handled in accordance to the EM&A Manual and relevant parties including the Engineer's Representative and IEC were informed of the complaints. The details of complaint are summarized as below:

A complaint was referred from EPD on 4 April 2011 about the daytime construction noise near Hoi Fai Road, Mong Kok. The complaint handling procedures in accordance with the EM&A Manual has been undertaken. It was investigated that the construction noise might be caused by construction activities of 805 contractor. Noise mitigation measure had been proposed and will be implemented before resuming the concerned construction work.

A complaint was referred from EPD on 12 April 2011 about the generation of muddy water from a West Kowloon Terminus construction site. The Contractor reviewed and investigated the case and the results were normal after checking the on-site wastewater treatment facilities and the quality of the discharge. However the Contractors were reminded to ensure that all the wastewater generated from the works should be diverted to the water treatment plant for treatment before discharge.

A complaint was referred from EPD on 20 April 2011 about the generation of concrete and mud stains from construction site near Man Wui Street at West Kowloon which affected the nearby carpark. The Contractor reviewed and investigated the case and it was caused by the piling works at the construction site. Proper mitigation measures have been implemented by the Contractor. The investigation results were reviewed by the IEC.

A complaint was referred from EPD on 26 April 2011 about the daytime construction noise generated from the construction site nearby Tower 5 of Sorrento at West Kowloon. Although no exceedance was recorded at the nearest monitoring

stations from the routine monitoring, the Contractor was reminded to improve the noise mitigation measures for the relevant construction works. The investigation results were reviewed by the IEC.

A complaint was referred from EPD on 29 April 2011 about the generation of construction noise between 7pm to 10pm on weekdays as well as on Sundays and holidays near the southern end of Austin Station. Upon the review and investigation, it was found that minor works were carried out by Contract 803A in the restricted hours with valid CNP. The use of PMEs complied with the requirement under the permit. In addition, frontline staff have been trained with reference to the compliance of the permit conditions. Besides, the Contractor has reminded to enhance the site management and provide proper mitigation measures for the construction works in order to minimize the construction noise to the nearby noise sensitive receivers.

7.2 Summary of Exceedance

In the reporting month, noise exceedances of air-borne noise Limit Level were recorded at Kong Tai Road Village House (CN 5) on 21 April 2011; HKIVE Haking Wong Waterfront Annex (CN 23) on on 6, 13 and 27 April 2011 (exceedance on 20 April was considered invalid as there was no school day); St. Mary's Church Mok Hing Yiu College (CN 25) on 7 April 2011; The Waterfront (CN 32) on 6, 20 and 29 April 2011 and The Arch (CN 33) on 7 April 2011.

For the noise exceedance at CN 5, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. Upon investigation, the exceedance might possible be due to construction works by 824 Contractor. The Contractor was reminded to provide noise mitigation measures to minimize the noise impact.

Regarding the noise exceedances at CN 23, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. The noise exceedance recorded on 6, and 27 April 2011 were caused by 805 site works, while the exceedance recorded on 13 April 2011 was mainly caused by other sources. The Contractor implemented mitigation measures to minimize the noise impact.

Regarding noise exceedance recorded at St. Mary's Mok Hiu Hing College (CN 25), actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractor were informed of the exceedance. It was found that pile removal work at Nam Cheong Launching Shaft near CN25 by Contractor 820 might have caused the noise exceedance. The Contractor was reminded to enhance the noise mitigation measures to minimize noise nuisance to the nearby NSRs.

For the noise exceedances at The Waterfront (CN 32) and The Arch (CN 33) in West Kowloon, actions identified in the Event and Action Plan (Table 3.4 of the EM&A Manual) were undertaken. The ER, IEC and Contractors were informed of the exceedances. The investigation result revealed that noise source may possibly due to works by 803A, 803B, 803D and 810B Contractors. Additional noise mitigation measures proposed by the Contractor were reviewed by IEC and ET and implemented by the 803A, 803B, 803D and 810B Contractors to minimize the noise impact. All contractors in WKT works area were reminded to enhance the noise mitigation measures to comply with the statutory requirement and minimize noise nuisance to the nearby NSRs.

In addition, there were two noise exceedances of Action Level triggered due to noise complaint during daytime hours received in the reporting month. Please refer to Section 7.1 above for details.

In the reporting month, there are exceedances of 24-hr TSP Action Level on 4 April 2011 at AM 3; 29 April 2011 at AM 4; 1 April 2011 at AM 15 and 1 April 2011 at AM17 were recorded in the reporting month. No exceedance of 24-hr TSP Limit Level was recorded in the reporting month. Actions stipulated under the Event and Action Plan (Table 9.4 of the EM&A Manual) were implemented for all exceedances and monitoring frequency was increased.

For the exceedance at AM 3, investigation results revealed that the exceedance might possibly due to construction work at Tai Kong Po Works Area. The 824 Contractor provided additional dust mitigation measures, including covering of stockpile, concreting the temporary slope and improving watering frequency and

coverage by automatic sprinklers. The situation would be continuously reviewed by IEC.

For the exceedance at AM 4, investigation results revealed that the exceedance might possibly due to site formation works at northern SSS area. The 823A Contractor was reminded to enhance the dust suppression measure including covering of stockpile and regular watering on haul road. The situation would be continuously reviewed by IEC.

For the exceedance at AM 15, investigation results revealed that the exceedance might possibly due to construction works near Lin Cheung Road Works Area. The 803A Contractor was reminded to enhance the dust suppression measure including covering of stockpile and regular watering on haul road. The situation would be continuously reviewed by IEC.

For exceedance at AM 17, investigation results revealed that the exceedance might possibly due to the traffic movement at the temporary material storage area opposite to Austin Road West. The 810B Contractor was reminded to watering the unpaved area more frequently. The situation would be continuously reviewed by IEC.

7.3 Summary of Notification of Summons, Prosecutions, Non-compliance and Corrective Actions

No notification of summons and prosecutions was received during the reporting month. No non-compliance event was recorded during the reporting period.

8. FUTURE KEY ISSUES

8.1 Construction Works in Coming Months

Works to be undertaken for the following months are summarized below.

Contract 802 (Works Area Q)
Sheet-pilling, bored pile removal, utility diversion, H-pile extraction, pile cap demolition and excavation & lateral supports
Contract 803A (Works Area V1)
Diaphragm wall construction, remedial works, concrete coring, utilities diversion and road works
Contract 803B (Works Area V1)
Socketted H-piling works, Loading test and interface coring for bored piles
Contract 803C (Works Area V1)
NIL (Contract Completed)
Contract 803D (Works Area V1)
Diaphragm wall, loading test, remedial works and concrete coring
Contract 805 (Works Area N & O)
Piers removal of footbridge, sheet piling works, cap demolition, and pile removal at CLP Spare Equipment Building,
Contract 805 (Works Area S)
Demolition of pile cap and sheet piling work
Demolition of pie cap, removal of footbridge, sheet-piling work
Contract 810B (Works Area V1 & U)
Site Clearance, Site Establishment, Hoarding Erection, Pre-drilling,

Excavation etc.
Contract 811A (Works Area V2)
Construction of diaphragm wall, H-pile and bored piles; traffic diversion at Lai Cheung Road; construction of traffic deck at Lai Cheung Road; external works to CLP Sub Station at Lai Cheung Road
Contract 811B (Works Area V2 & Y)
Construction for diaphragm wall, bored piling and H-piles, temporary road construction, construction of temporary footbridge; culvert diversion; operation of Nam Cheong Barging Point
Contract 820 (Works Area L)
Nil
Contract 820 (Works Area M)
Concreting; Plant de-mobilization; Excavation Work; Grouting
Contract 820 (Works Area P)
Diaphragm wall construction for Box B including breaking and concreting work; Pre-bored H-pile at Box B; Grouting work; Utility diversion; Bulk Excavation for the shaft; Pile Removal Work
Contract 820 (Works Area Q)
Temporary traffic arrangement
Contract 820 (Works Area R)
Utilities diversion
Contract 820 (Works Area S)
Utilities diversion; Excavation Work; Surface re-instatement
Contract 820 (Works Area Y)
Barging Point site setup

Contract 820 (Works Area V2)
Ground treatment works
Contract 821 (Works Area J)
Pipe work for the water-recycling and treatment system, set up of maintenance workshop, blasting, breaking & drilling work at the portal.
Contract 821 (Works Area Y)
Operation of the barging point
Contract 822 (Works Area F)
Adit construction, construction of pipe pile wall, retaining wall construction
Contract 822 (Works Area G)
Construction of pipe pile wall,
Contract 822 (Works Area H)
Adit construction, preparation work of conveyor erection
Contract 822 (Works Area AC)
Nil
Contract 822 (Works Area AE)
Nil
Contract 822 (Works Area AG)
Nil
Contract 823A (Works Areas D and D1)
Site formation, pre-drilling works
Contract 823A (Works Area E)

Pre-drilling works, construction of haul road
Contract 823B (Works Areas D)
Site formation, pre-drilling works, site office erection
Contract 823B (To Kau Wan Works Areas)
Nil
Contract 823B (Works Areas Z)
Site formation, wheel washing and barging facility set up
Contract 824 (Works Area B)
Bored piling works
Contract 824 (Works Area C)
Pipe piling works at Tai Kong Po Works Area; bridge construction at access road
Contract 824 (Works Area AF)
Nil
Contract 825 (Works Area A)
Shaft construction
Contract 825 (Works Area AA)
Nil

Table 8-1 Summary of construction works in coming months

According to the latest programme, no construction would be commenced at new works area in coming month. Impact monitoring would be continued according to the construction programme.

8.2 Monitoring Schedule for Next Month

The tentative schedule of TSP, noise and ecological monitoring for the next reporting period is presented in Appendix E.

8.3 Stage 1 Ground Treatment Works at Hoi Wang Road near Hoi Yu House of Hoi Fu Court and Block 8 of Charming Garden

Regarding the Stage 1 ground treatment works by jet grouting at Hoi Wang Road near Hoi Yu House of Hoi Fu Court and Block 8 of Charming Garden, as the site layout was updated since last reporting month, the updated noise source locations on the layout and corresponding mitigation measures from the proposed grouting works have been assessed and updated by the Contractor. The assessment results show that no significant adverse impacts due to Stage 1 ground treatment works.

9. CONCLUSIONS

The Report presents the results of EM&A works and the impact monitoring for the construction works of the XRL project undertaken during the period of 1 April 2011 to 30 April 2011. The major construction activities in the reporting period included foundation works in the West Kowloon Works Areas, Nam Cheong, Kwai Chung, Shing Mun, Shek Yam, Pat Heung, Tai Kong Po, Ngau Tam Mei, Mai Po Works Area and Barging Points.

Impact monitoring for air quality and noise were conducted in accordance with the EM&A Manual in the reporting period. Exceedances of Limit Level in noise monitoring were recorded at Kong Tai Road Village House (CN 5), HKIVE Haking Wong Waterfront Annex (CN 23), St. Mary's Church Mok Hing Yiu College (CN 25), The Waterfront (CN 32) and The Arch (CN 33). There were two Action Level exceedances in noise monitoring in the reporting month. Exceedances of 24-hour TSP Action Level were recorded at Kong Tai Road Village House (AM3), DD110 LOT 482, Wang Toi Shan (AM 4), between Sorrento and The Waterfront (AM 15) and The Victoria Towers (AM 17) in the reporting month. There was no exceedance of 24-hour TSP Limit Level. Dust source was identified and the contractor improved mitigation measures accordingly to minimize the dust impact. No environmental notification of summon and prosecution was received in the reporting period.

Five environmental complaints were received in the reporting period. The environmental complaints received were related to construction noise from construction site near Hoi Fai Road; generation of muddy water from WKT works area; generation of mud stain from works area near Man Wui Street; construction noise from WKT works area near Sorrento; construction noise from WKT Works Area near Austin Station. The complaints had been handled in accordance with the procedures stipulated in the EM&A Manual. Investigations were carried out in accordance with the EM&A Manual.


Site inspections were conducted regularly to monitor proper implementation of environmental pollution control and mitigation measures for the Project. No non-compliance to the environmental requirements was identified in the reporting


period.


In the reporting period, there was no reporting change of circumstances which may affect the compliance with the recommendations of the EIA Report. It is concluded from the environmental monitoring and audit works for the XRL Project that the construction works were undertaken in an appropriately environmentally sensitive manner in the reporting period. The environmental protection and pollution control measures provided by the contractors were generally acceptable apart from some irregularities which were responded by the respective civil works contractors. The ET would continue the implementation of the environmental monitoring and audit programme in accordance to the EM&A Manual and to a level consistent with MTRCL's Corporate Sustainability Policy.


Appendix A


Works Area

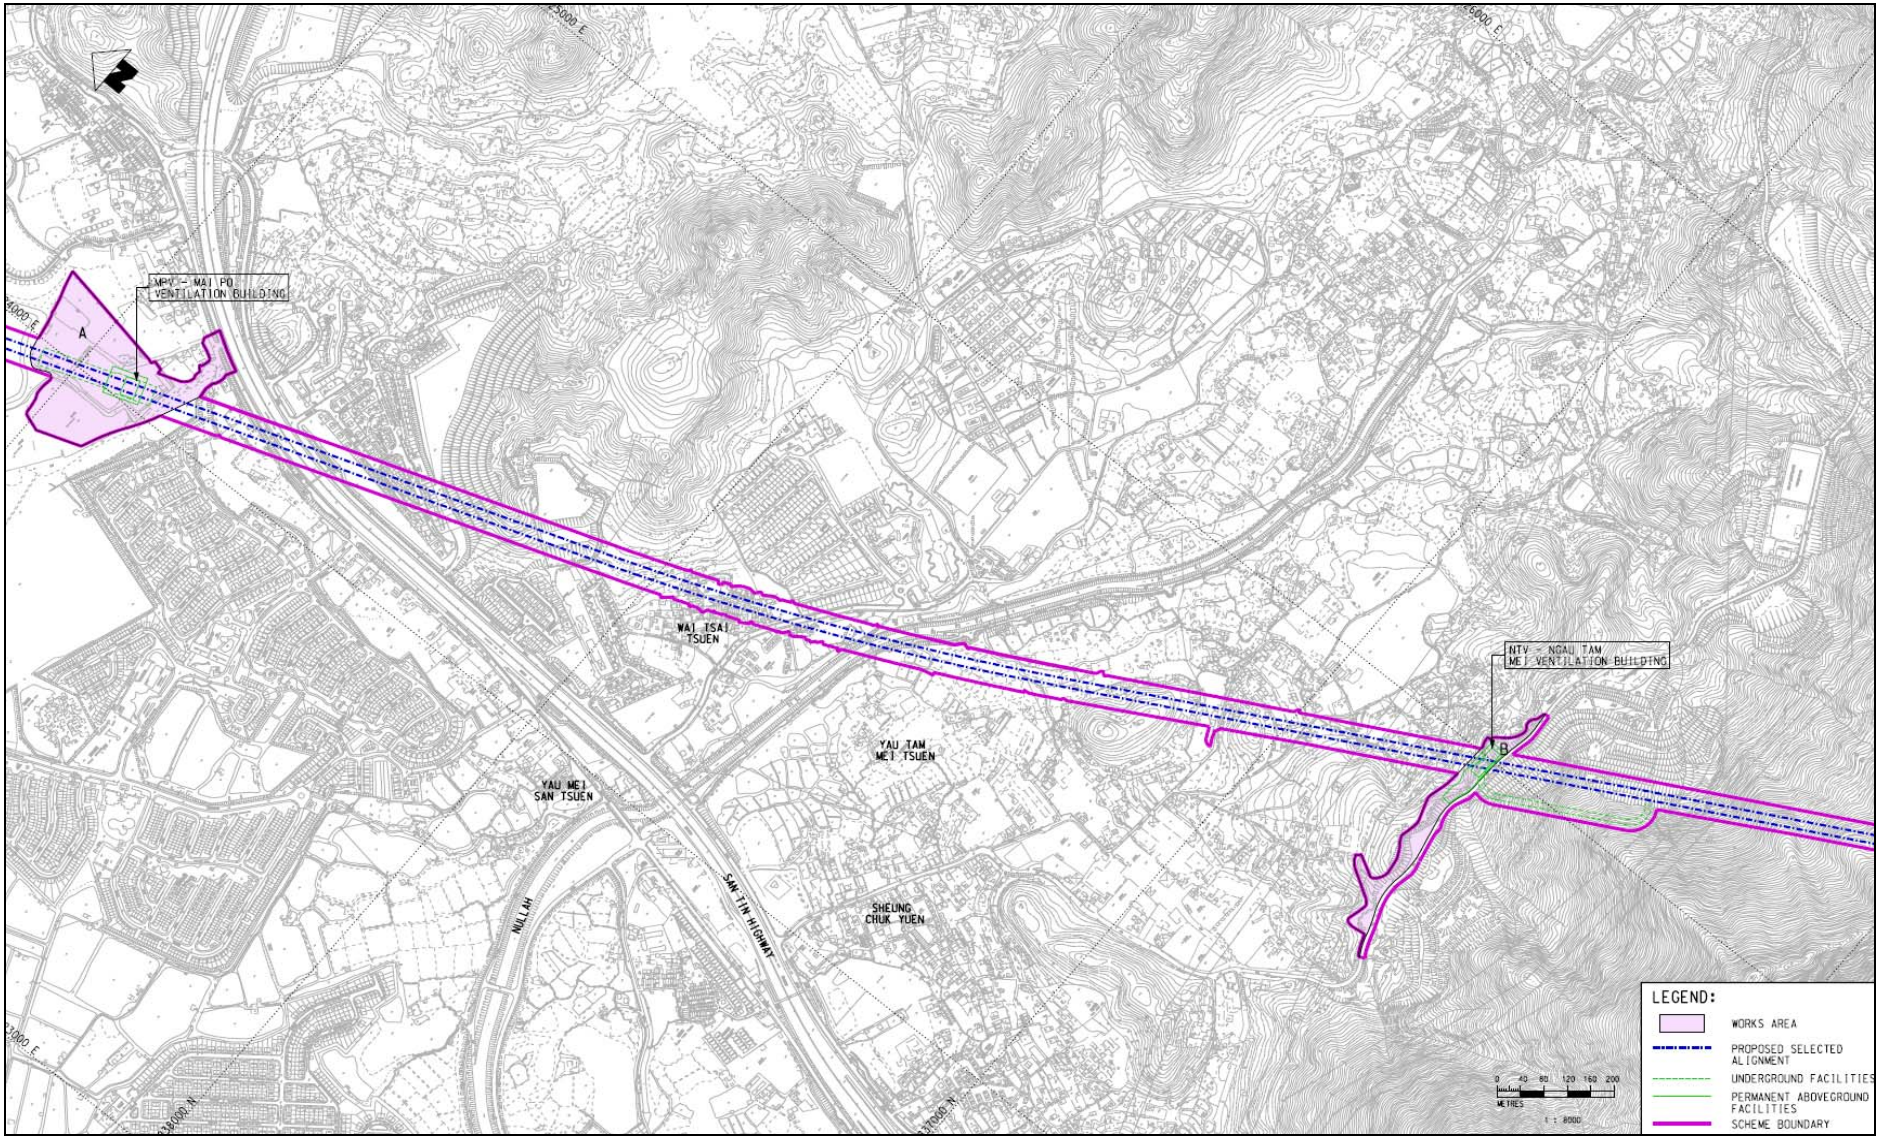

MPV - MAI PO VENTILATION BUILDING
A
NTV - NGAU TAM MEI VENTILATION BUILDING
B
WAI TSAI TSUEN
YAU TAM MEI TSUEN
YAU MEI SAN TSUEN
SHEUNG CHUK YUEN
NULLAH
SAN TIN HIGHWAY
LEGEND:
WORKS AREA
PROPOSED SELECTED ALIGNMENT
UNDERGROUND FACILITIES
PERMANENT ABOVEGROUND FACILITIES
SCHEME BOUNDARY
METRES
1 : 8000

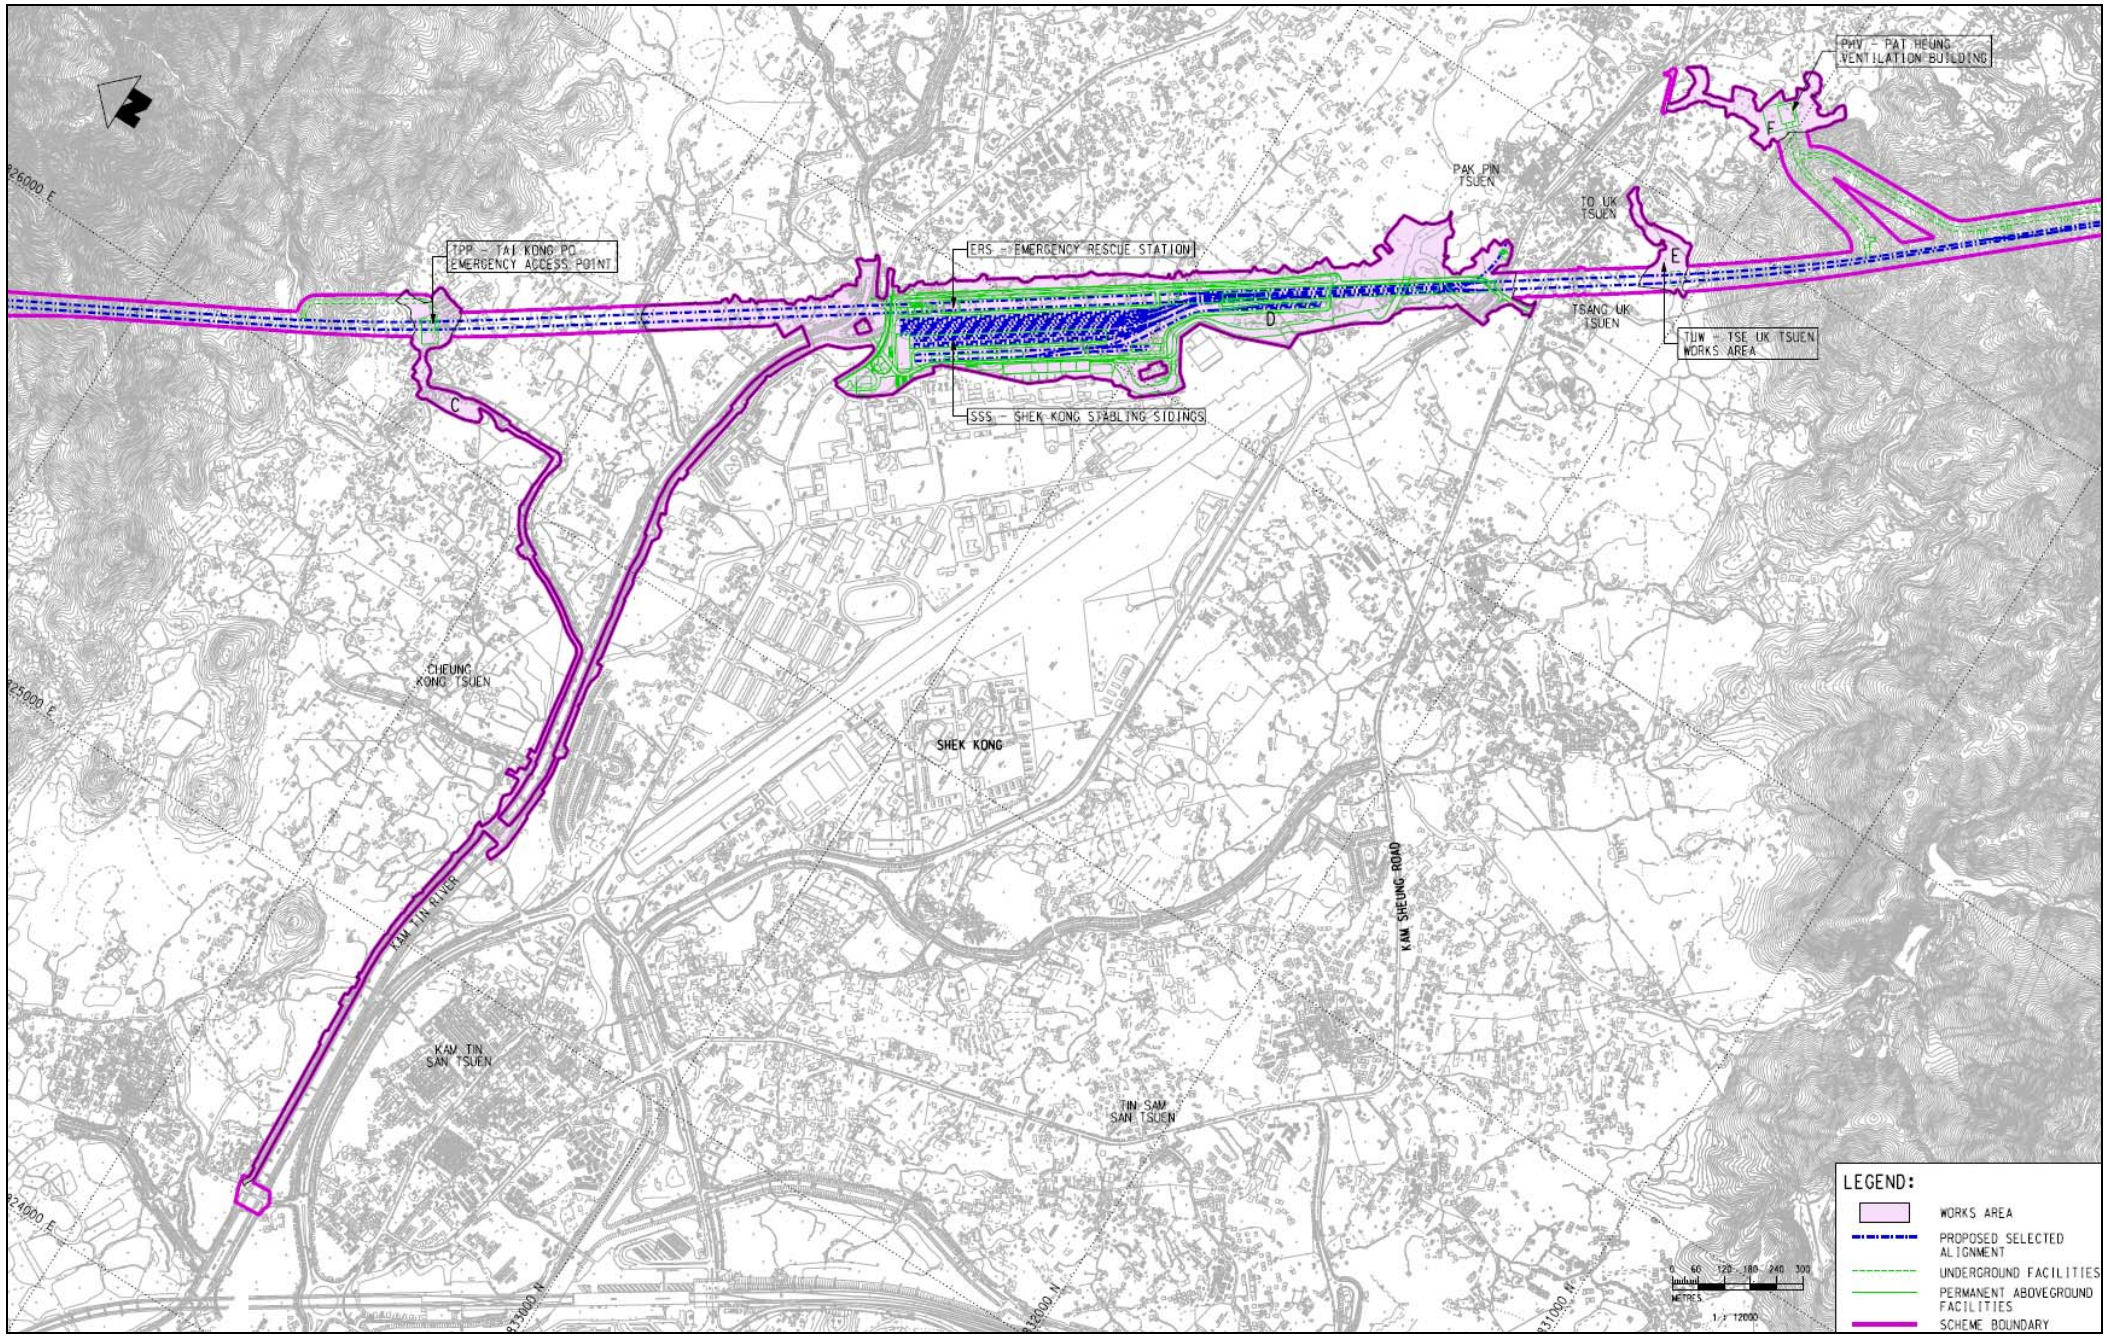

PHV – PAT HEUNG VENTILATION BUILDING
PAK PIN TSUEN
TO UK TSUEN
TSANG UK TSUEN
TUW – TSE UK TSUEN WORKS AREA
TPP – TAI KONG PO EMERGENCY ACCESS POINT
ERS – EMERGENCY RESCUE STATION
SSS – SHEK KONG STABLING SIDINGS
CHEUNG KONG TSUEN
SHEK KONG
KAM TIN RIVER
KAM SHEUNG ROAD
KAU TIN SAN TSUEN
TIN SAM SAN TSUEN
C
D
E
F
826000 E
825000 E
824000 E
833000 N
832000 N
831000 N
0 60 120 180 240 300
METRES
1 : 12000
LEGEND:
WORKS AREA
PROPOSED SELECTED ALIGNMENT
UNDERGROUND FACILITIES
PERMANENT ABOVEGROUND FACILITIES
SCHEME BOUNDARY

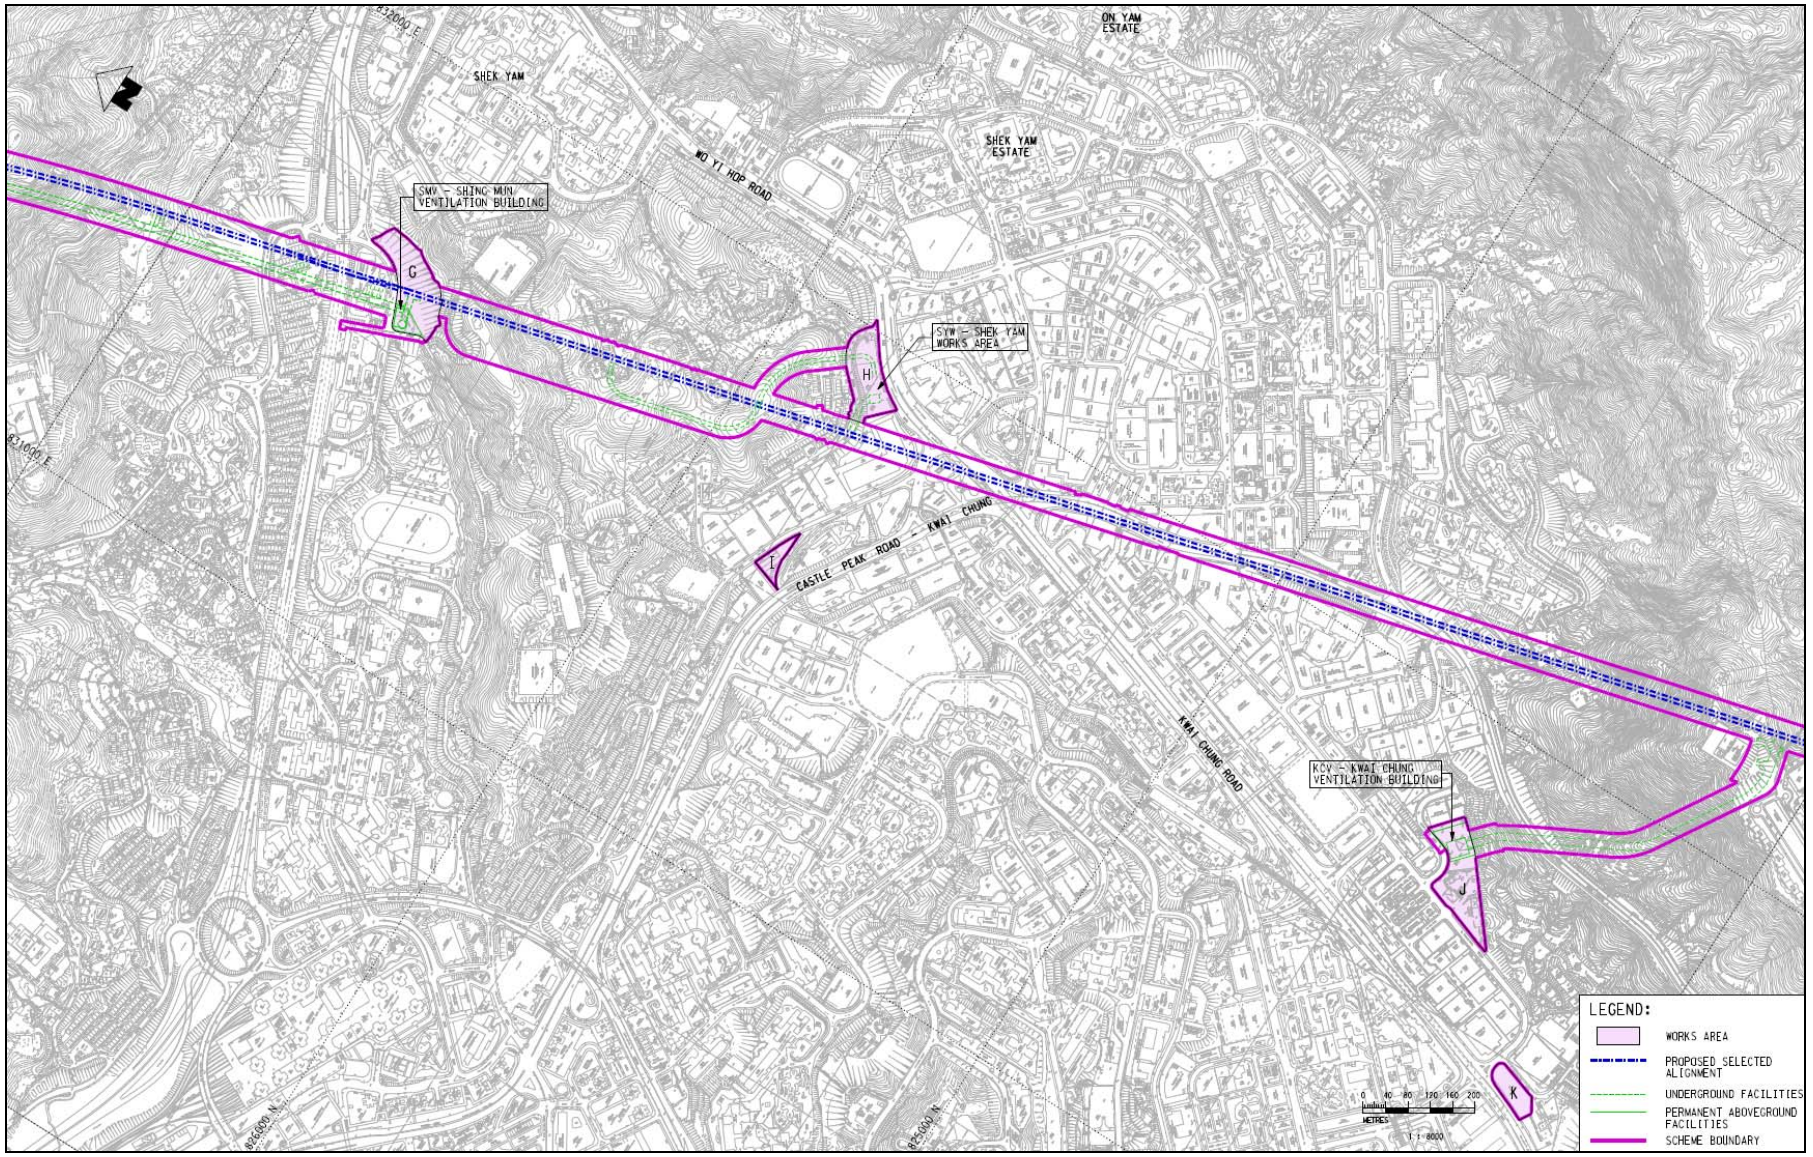

SHEK YAM
ON YAM ESTATE
SHEK YAM ESTATE
WO YI HOP ROAD
SMV - SHING MUN VENTILATION BUILDING
SYW - SHEK YAM WORKS AREA
CASTLE PEAK ROAD - KWAI CHUNG
KWAI CHUNG ROAD
KCV - KWAI CHUNG VENTILATION BUILDING
G
H
I
J
K
831000 E
832000 E
826000 N
825000 N
0 40 80 120 160 200
METRES
1 : 8000
LEGEND:
WORKS AREA
PROPOSED SELECTED ALIGNMENT
UNDERGROUND FACILITIES
PERMANENT ABOVEGROUND FACILITIES
SCHEME BOUNDARY

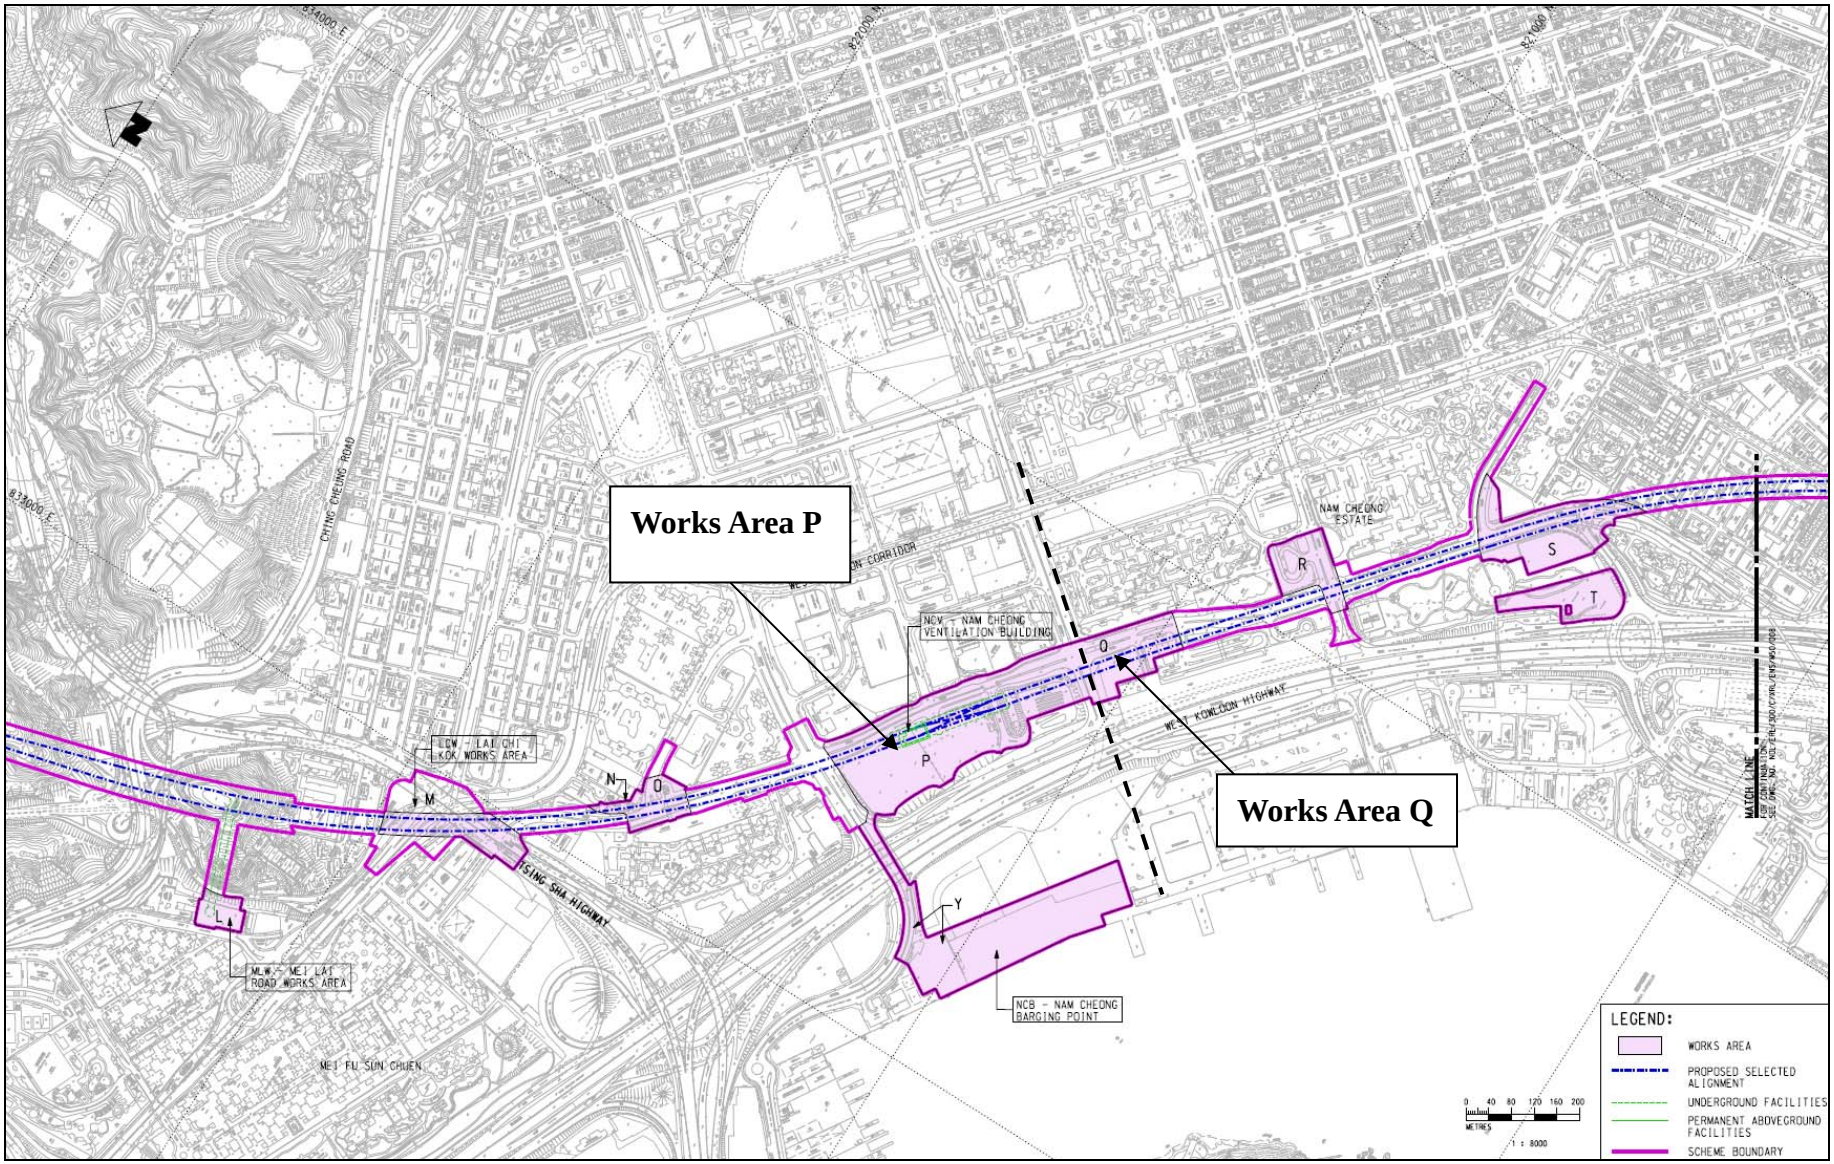
Works Area P
Works Area Q
CHING CHEUNG ROAD
NAM CHEONG ESTATE
NCV - NAM CHEONG VENTILATION BUILDING
WEST KOWLOON HIGHWAY
LCW - LAI CHI KOK WORKS AREA
TSING SHA HIGHWAY
MLW - MEI LAI ROAD WORKS AREA
NCB - NAM CHEONG BARGING POINT
MEI FU SUN CHUEN
MATCH LINE
LEGEND:
WORKS AREA
PROPOSED SELECTED ALIGNMENT
UNDERGROUND FACILITIES
PERMANENT ABOVEGROUND FACILITIES
SCHEME BOUNDARY

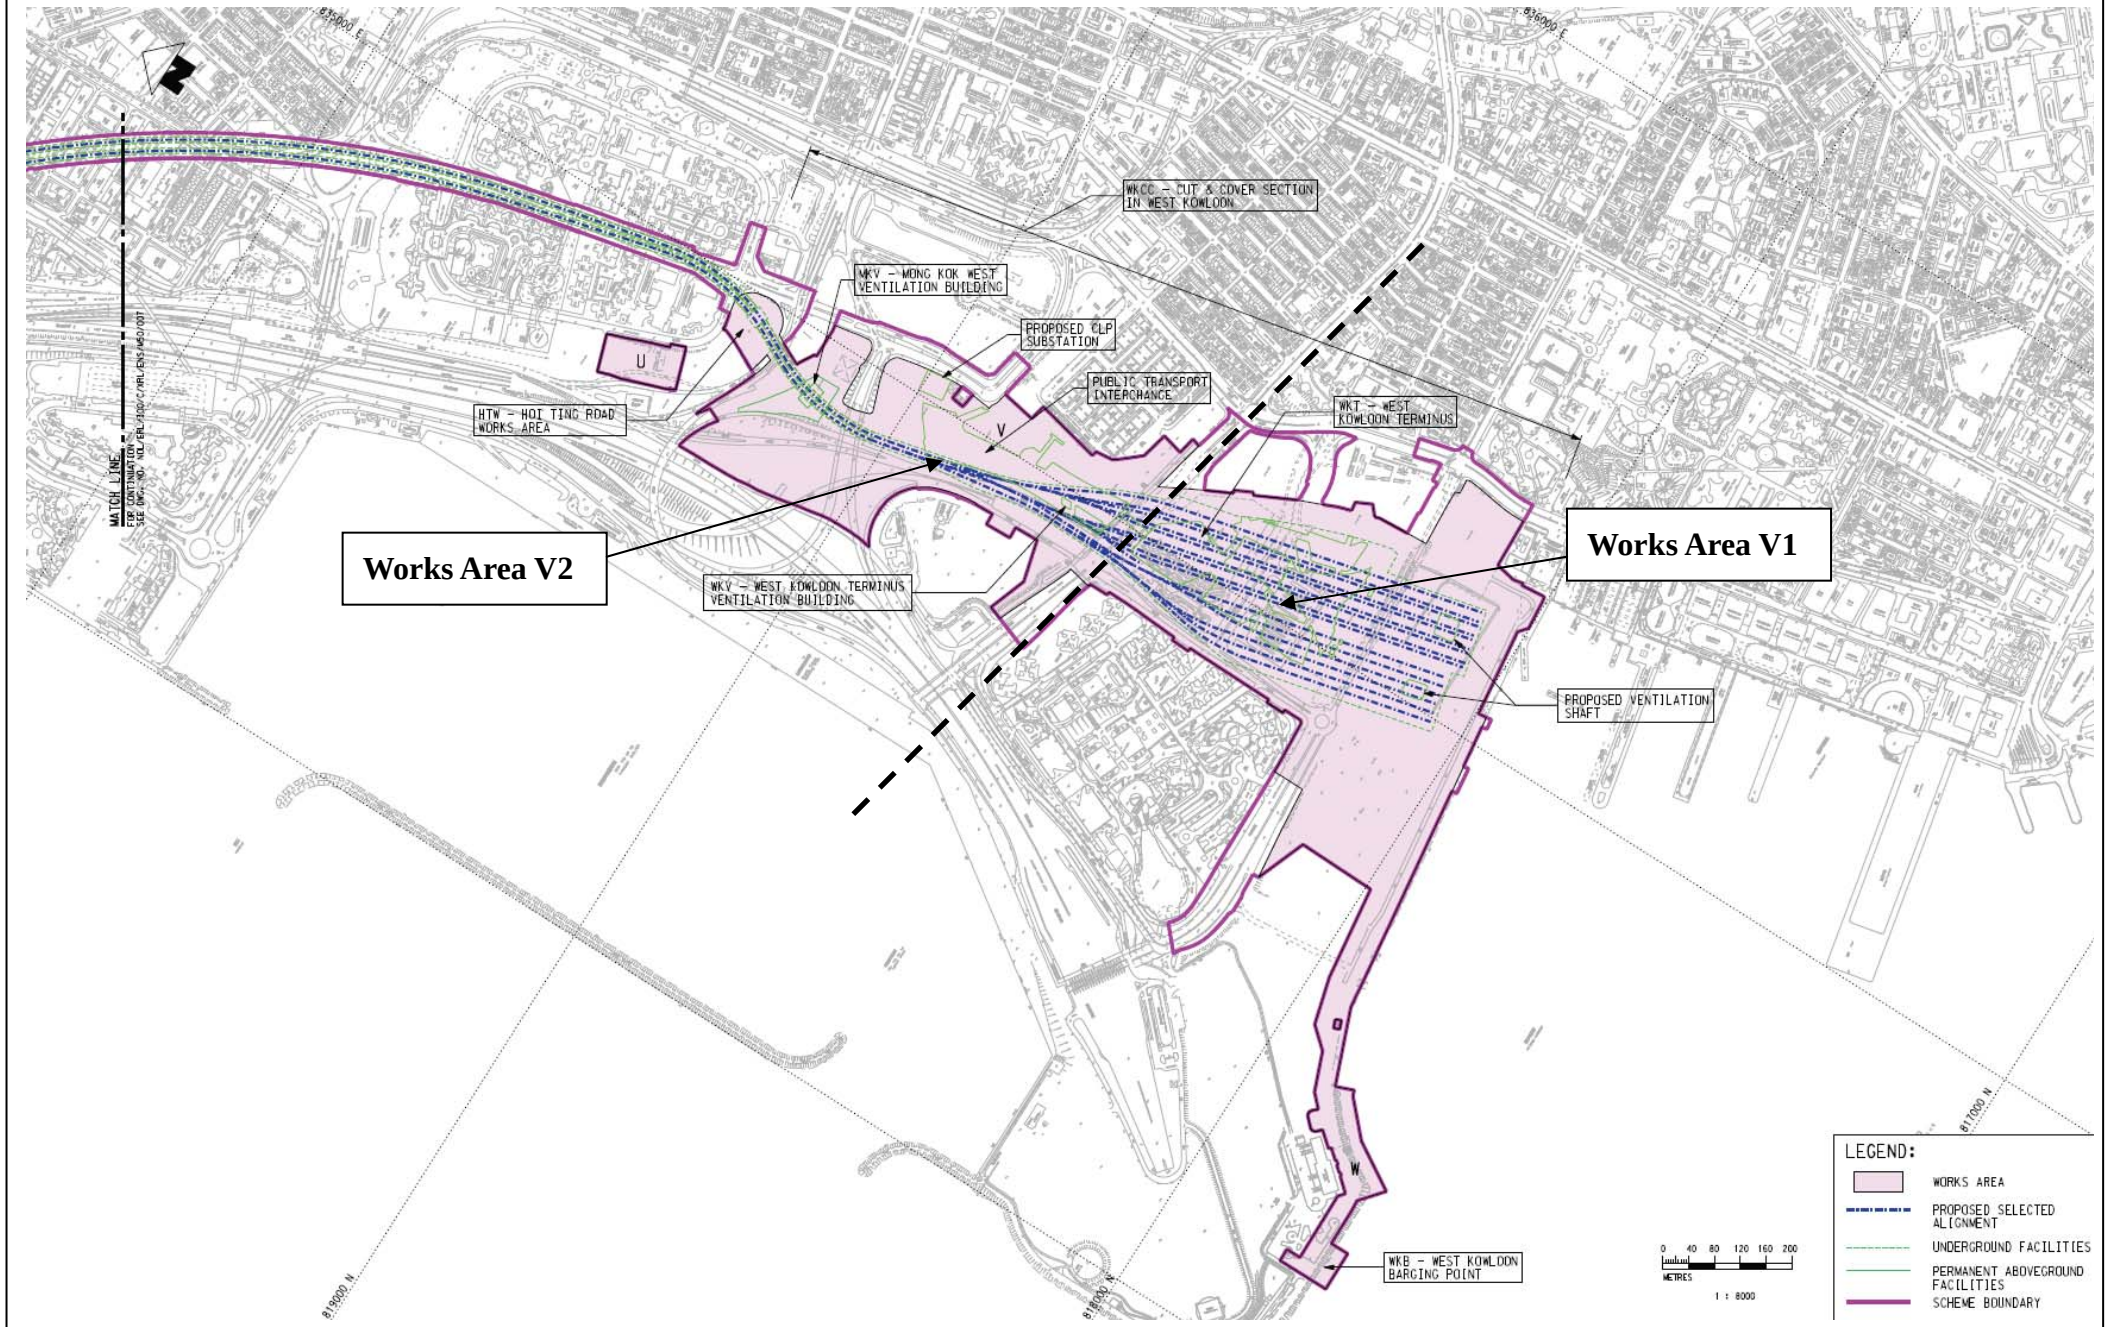

WKCC - CUT & COVER SECTION IN WEST KOWLOON
WKV - MONG KOK WEST VENTILATION BUILDING
PROPOSED CLP SUBSTATION
PUBLIC TRANSPORT INTERCHANGE
WKT - WEST KOWLOON TERMINUS
HTW - HOI TING ROAD WORKS AREA
MATCH LINE FOR CONTINUATION SEE DWG. NO. MEL/800/CIVIL/EKS/WSO/001
Works Area V2
Works Area V1
WKV - WEST KOWLOON TERMINUS VENTILATION BUILDING
PROPOSED VENTILATION SHAFT
WKB - WEST KOWLOON BARGING POINT
U
V
W
836000 E
818000 N
LEGEND:
WORKS AREA
PROPOSED SELECTED ALIGNMENT
UNDERGROUND FACILITIES
PERMANENT ABOVEGROUND FACILITIES
SCHEME BOUNDARY
0 40 80 120 160 200
METRES
1 : 8000

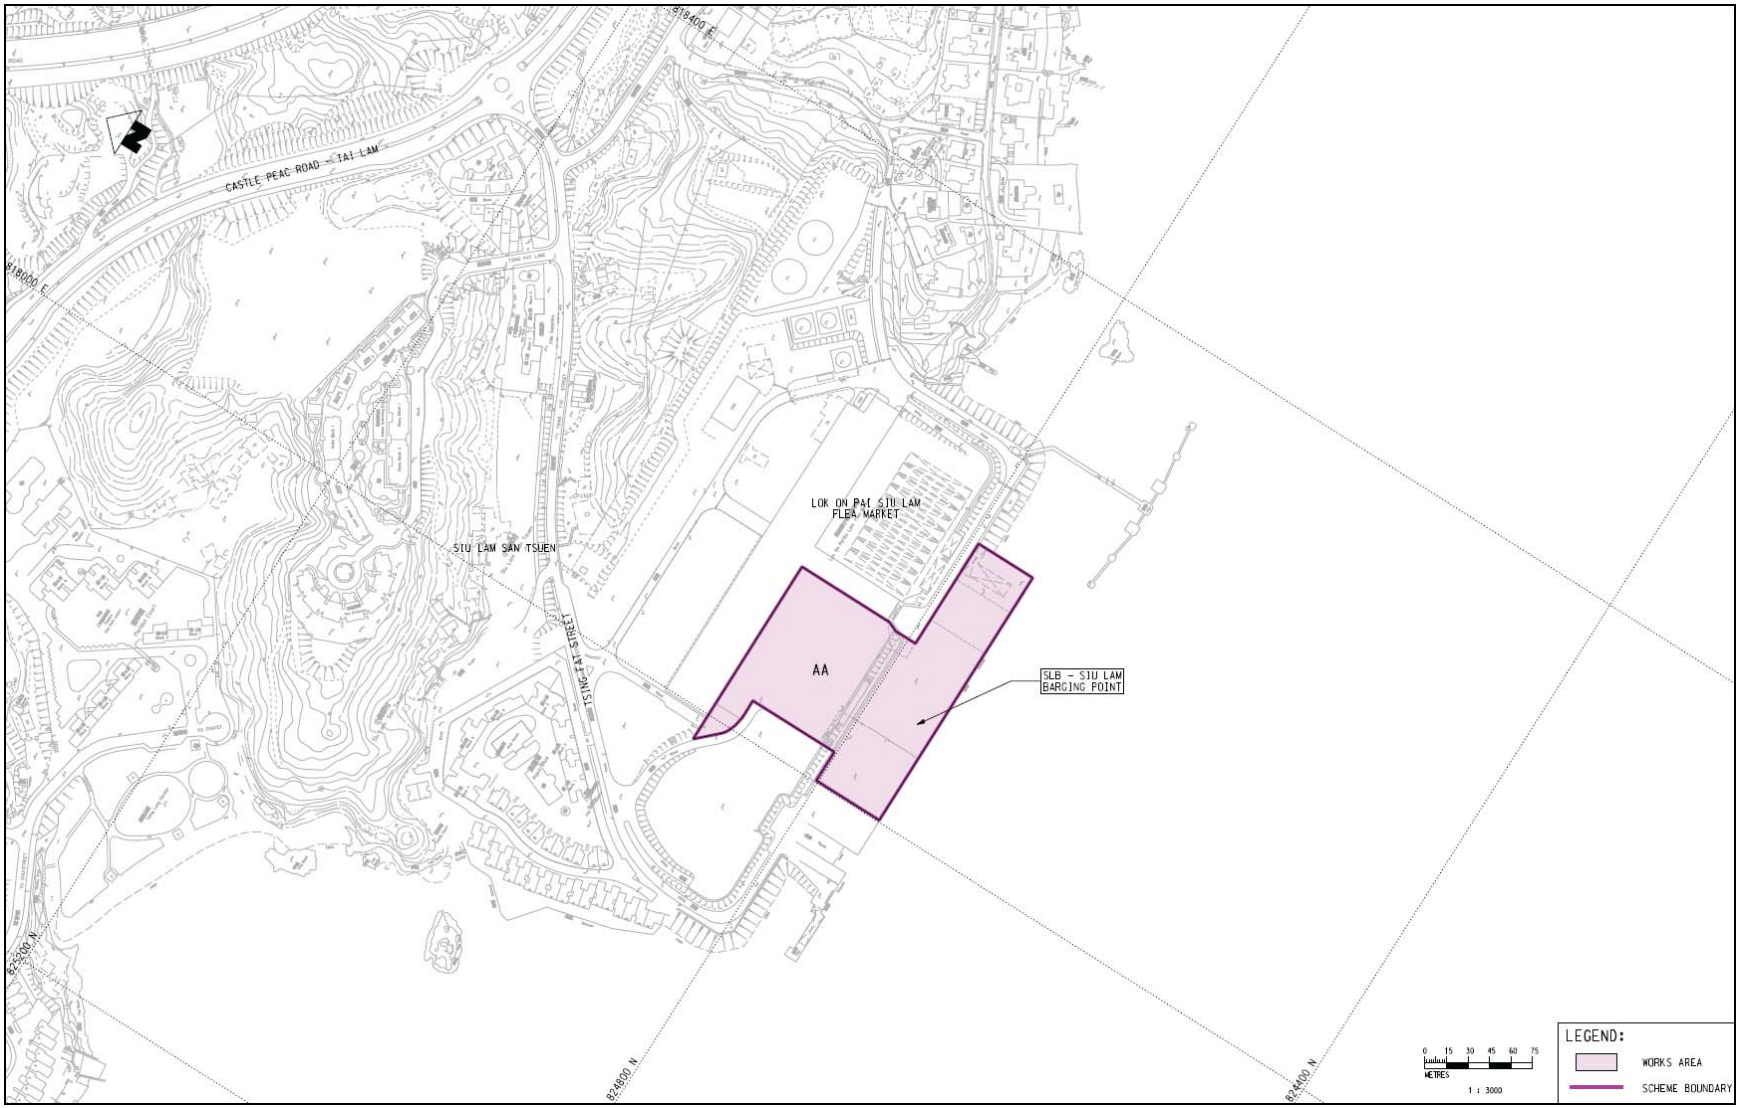
818400 E
CASTLE PEAK ROAD - TAI LAM
818000 E
LOK ON PAI SIU LAM
FLEA MARKET
SIU LAM SAN TSUEN
TSING FAT STREET
AA
SLB - SIU LAM
BARGING POINT
825000 N
824800 N
824400 N
0 15 30 45 60 75
METRES
1 : 3000
LEGEND:
WORKS AREA
SCHEME BOUNDARY

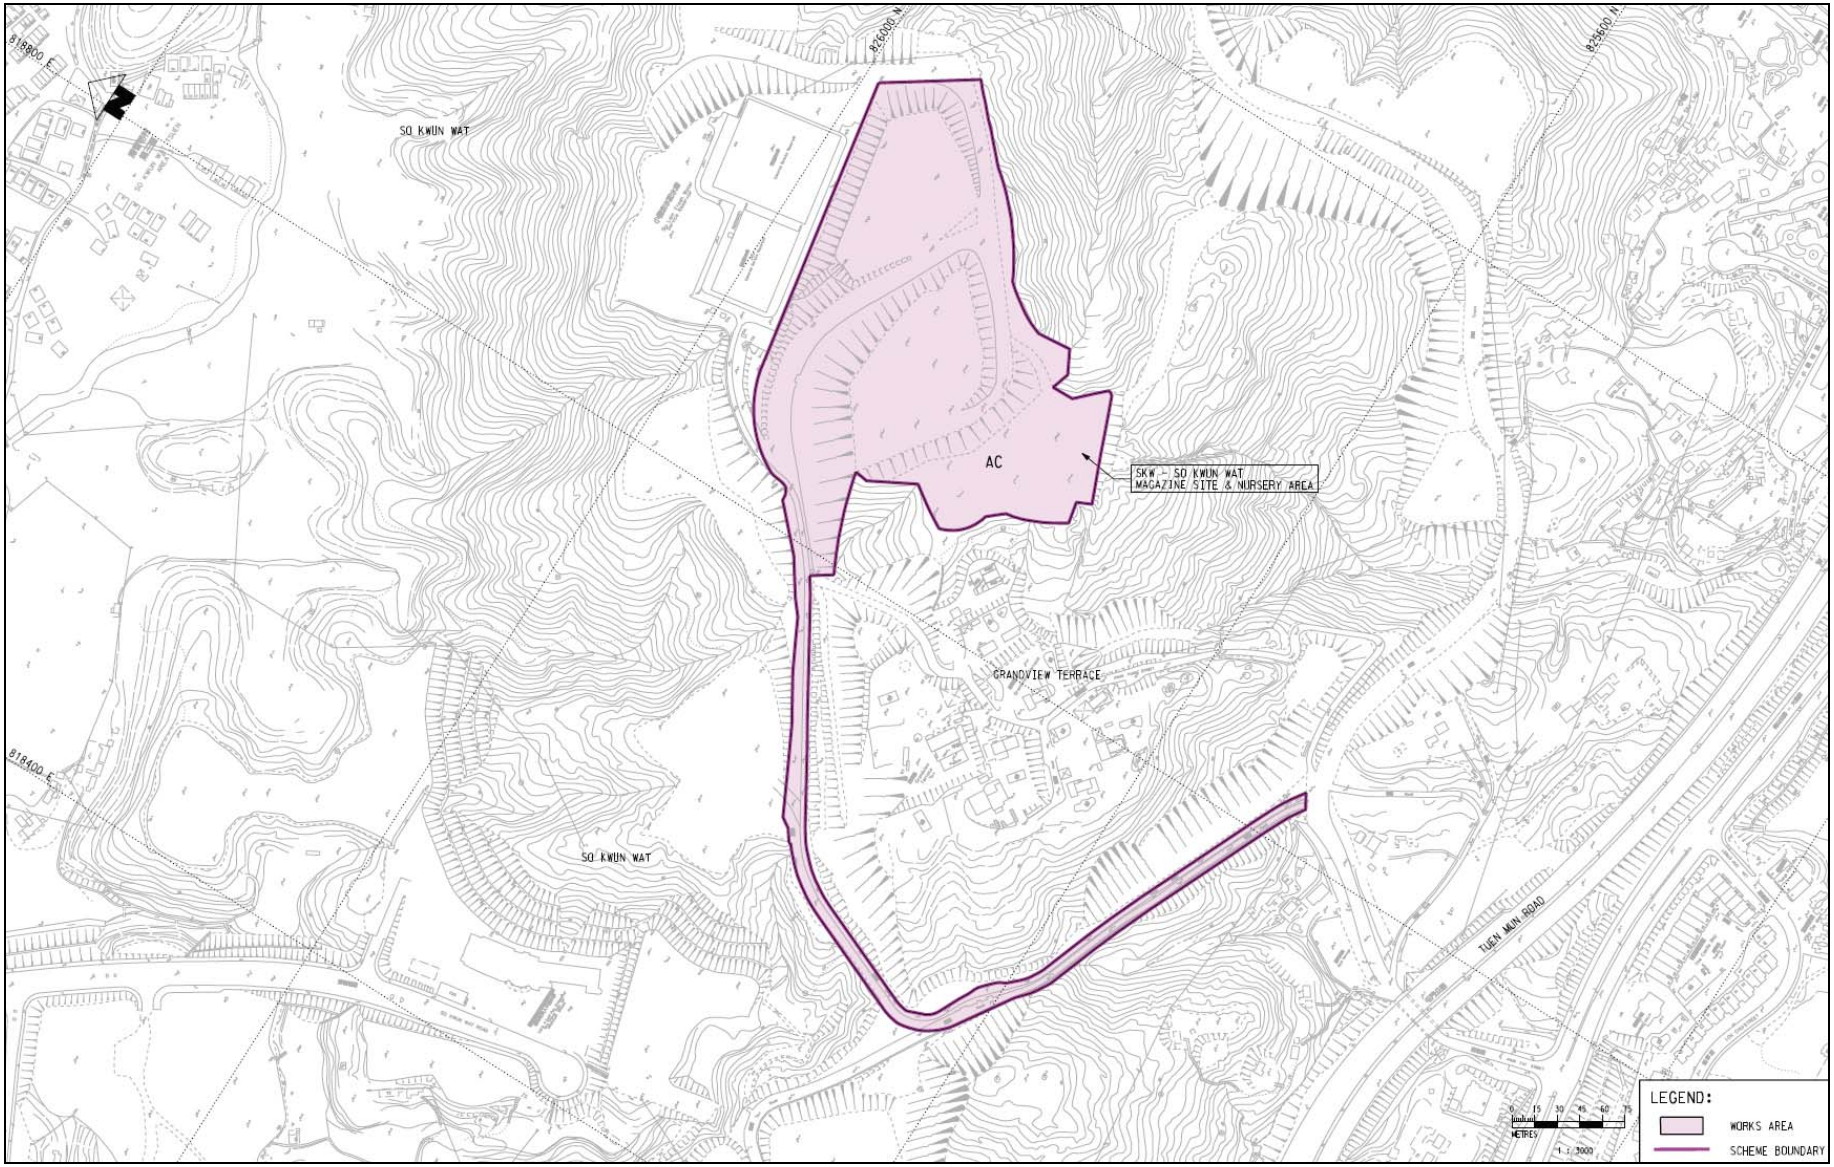
818800 E
818400 E
836600 N
836200 N
SO KWUN WAT
SO KWUN WAT
SO KWUN WAT
AC
SKW - SO KWUN WAT
MAGAZINE SITE & NURSERY AREA
GRANDVIEW TERRACE
TUEN MUN ROAD
0 15 30 45 60 75
METRES
1 : 3000
LEGEND:
WORKS AREA
SCHEME BOUNDARY

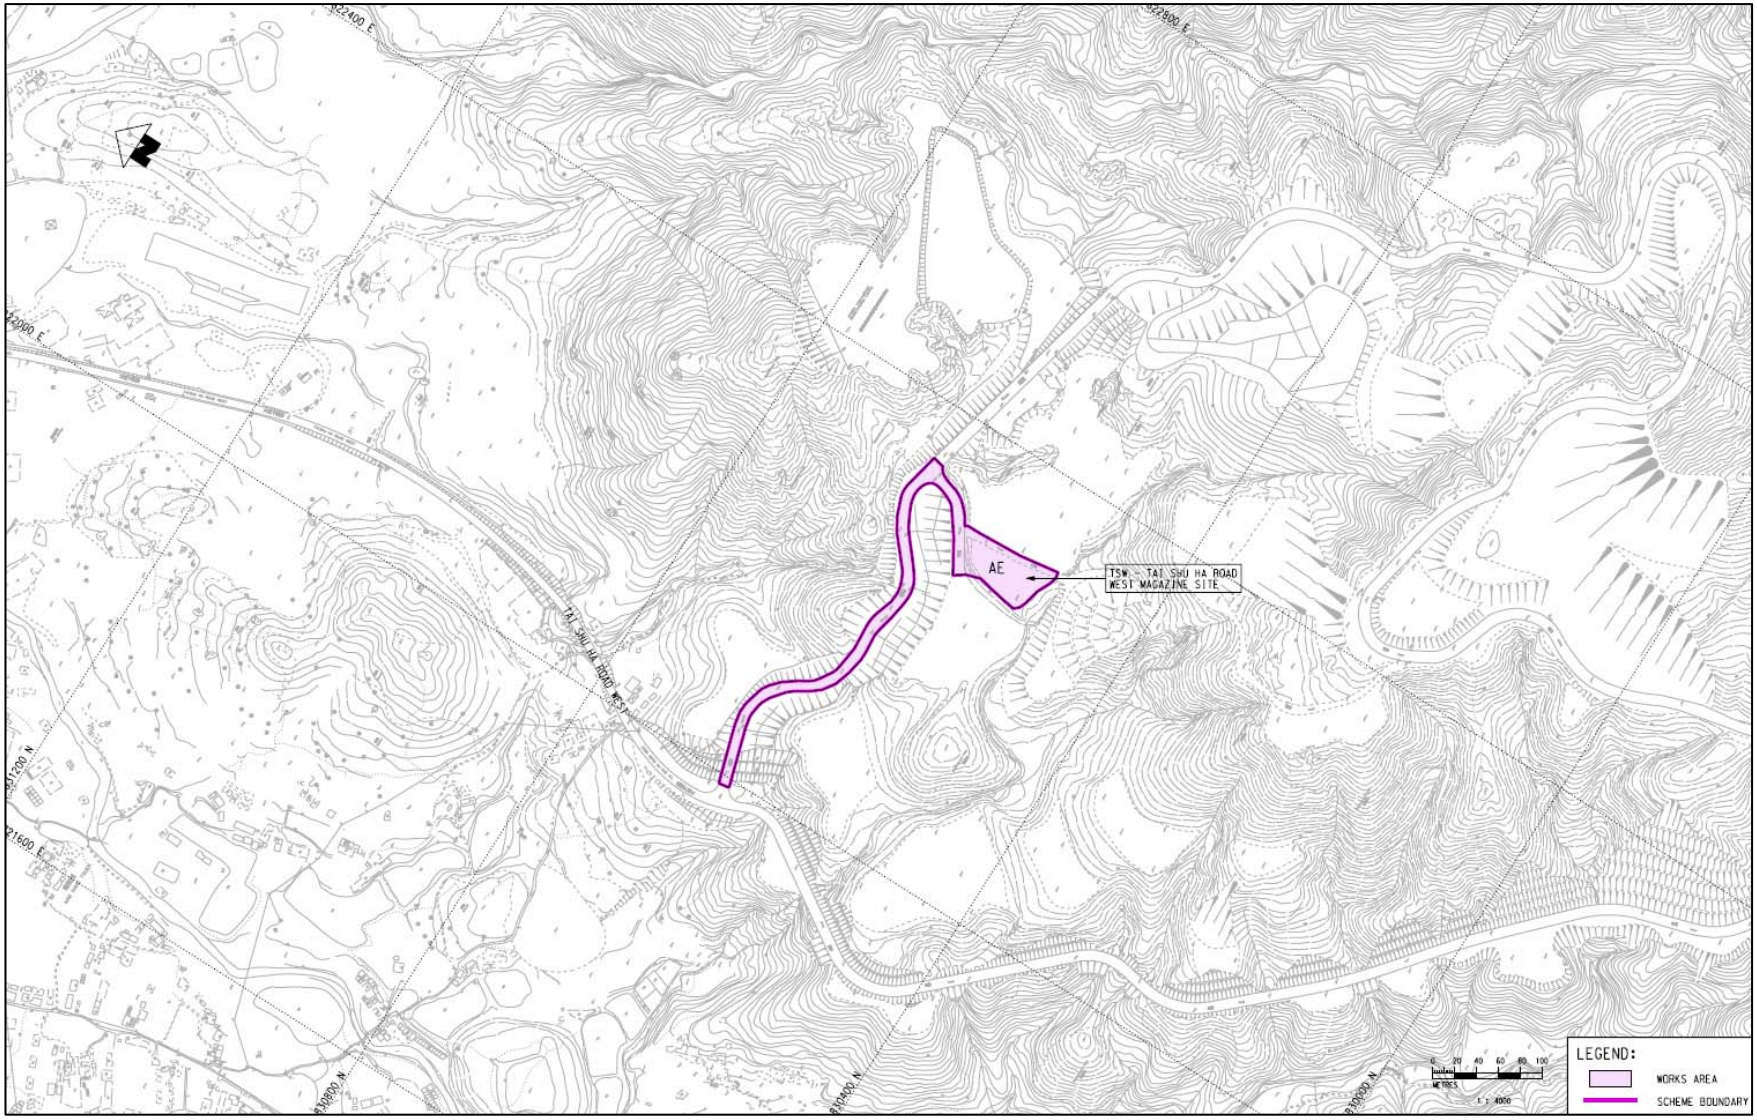
822400 E
822800 E
821200 E
821600 E
810800 N
810400 N
810000 N
AE
TSW - TAI SHU HA ROAD WEST MAGAZINE SITE
TAI SHU HA ROAD WEST
0 20 40 60 80 100
METRES
1 : 4000
LEGEND:
WORKS AREA
SCHEME BOUNDARY


821600 E
822000 E
822400 E
22400 N
22000 N
TSING CHAU WAN
TSING CHAU WAN
AG
TCB - TSING CHAU TSAI BARGING POINT
TOLL PLAZA
AIRPORT EXPRESS
NORTH LANTAU HIGHWAY
TSING CHAU TSAI
0 15 30 45 60 75
LEGEND:

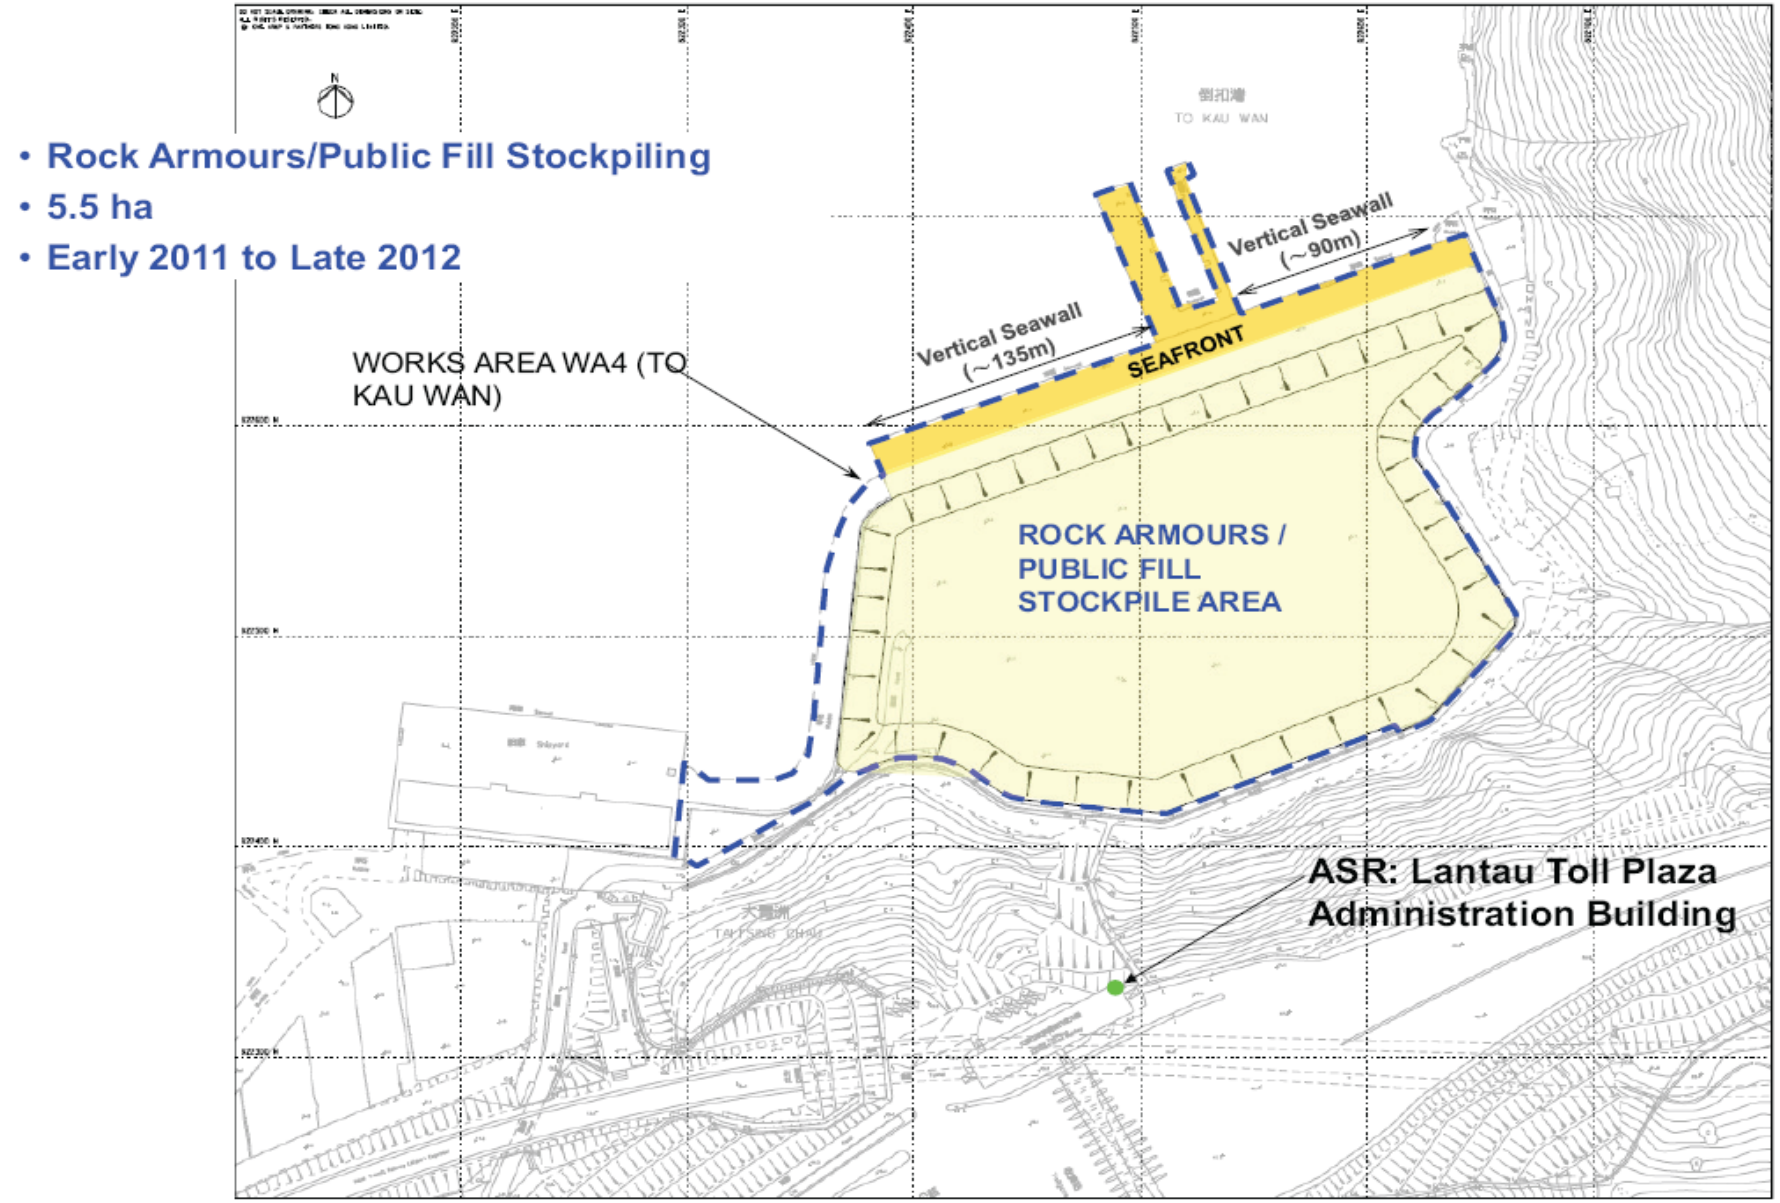

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link Environmental Review Report – Stock Piling Facility in To Kau Wan	SCALE	N.T.S.	DATE	Dec-10
	Location Plan for To Kau Wan Stockpiling Area	DRAWING NO.	Figure 2.1		

Appendix B

Project Management Organization and Contacts of Key Personnel

Title	Name	Telephone
Engineer's Representative		
Construction Manager (802, 805, 820 & 821)	Mr. Bill Clowes	3605 0056
Construction Manager (803 A/B)	Mr. Samuel Lo	3575 5641
Construction Manager (803 D & 810 B)	Mr. KS Lim	3575 5723
Construction Manager (811 A & B)	Mr. Albert Lam	3575 1357
Construction Manager (822, 823 A & 823B)	Mr. Andy Fok	2208 3732
Construction Manager (824 and 825)	Mr. Ivan Chau	2208 3334
Independent Environmental Checker		
Divisional Manager	Dr. Anne Kerr	2828 5793
Environmental Team		
Environmental Team Leader	Mr. Glenn Frommer	2688 1552
Deputy Environmental Team Leader	Mr. Richard Kwan	2688 1179
Contractor		
Contract 802 Contractor		
Project Manager	Frankie Lam	6021 2602
Project Quality and Environmental Manager	Ms. Jasmine Tso	2360 0719
Contract 803A Contractor		
Project Manager	Dick YIU	9426 4657
Site IMS Manager	Nick LAU	9216 9245
Contract 803B Contractor		
Project Manager	Fung Lai Man	9252 4204
Environmental Officer	Mr. C.K. Yau	9203 6046

Title	Name	Telephone
Contract 803D Contractor		
Project Manager	Dick YIU	9426 4657
Site IMS Manager	Nick LAU	9216 9245
Contract 805		
Project Manager	Hobby LAU	9828 0638
Environmental Engineer / Officer	Federick WONG	6330 0519
Contract 810B Contractor		
Project Director	Mr. Smollett LEE	6629 4441
Environmental Manger	Mr. Calvin SZE	9205 9277
Contract 811A Contractor		
Project Manager	Bob Aylmer	2561 8072
Quality, Safety and Environmental Manager	Keith Gordon	3994 8345
Environmental Officer	Kevin Wong	2164 2832
Contract 811B Contractor		
Project Manager	Chris Williams	9669 2665
Construction Manager	Anthony Zervaas	6011 8178
Environmental Manager	Brian Kam	9456 9541
Environmental Officer	Sammie Chan	6407 3833
Contract 820 & 821 Contractor		
Project Director	Alain Hervio	2215 6600/ 6112 9197
Senior QSE Manager	Y. T. So	2215 6631/ 9307 8728
820 Environmental Officer	Marcus Cheung	2215 6632
821 Environmental Officer	Shelton Chan	3608 0808

Title	Name	Telephone
Contract 822 Contractor		
Environmental & Quality Manager	Mr. Brian Pickering	6323 5753
Environmental Manager / Officer	Mr. David Hung	9765 6151
Environmental Coordinator	Ms. Jane Huang	6491 4620
Contract 823A & B Contractor		
Project Manager	Philip Davies	2411 7600
Environmental Officer	Wendy Ng	2411 7608
Contract 824 Contractor		
Works Manager	Ian Sweeney	9759 8192
Environmental Officer	Patrick Sin	6022 8646
Contract 825 Contractor		
Project Manager	Mr. Nakayama	2482 8101
Environmental Manager	Mr. Kenneth Lau	9723 4718

Appendix C

Implementation Status

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Ecological Impact (Detailed design Phase / Pre-construction Phase)						
S3.398	- Prior to commencement of channel works, an ecological habitat management plan should be prepared to provide the detailed specifications for the habitats and ecological functions to be provided, and control of colonization of invasive plant species at the mitigation stream habitats and define the long-term management and ecological monitoring and audit requirements for these habitats.	To mitigate the avoidable loss of watercourse habitat	MTR	SSS	Detailed design phase / Prior to commencement of channel works	Ecological Habitat Management Plan (EHMP) formulated and submitted to EPD
S3.388 - S3.397	- The constructed channel in the SSS site should include open channel with ecologically friendly stream feature to mitigate the direct impact due to the loss of a watercourse habitat in Shek Kong.	To mitigate the avoidable loss of watercourse habitat	MTR / DDC	SSS	Detailed design phase	AFCD's comment has been sought during formulation of the EHMP

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S3.410	- The implementation details of the impact monitoring programme should be described in ecological monitoring plan for EPD approval before commencement of construction activities.	To outline details of ecological impact monitoring	MTR	MPV, TPP, SSS / ERS, PHV and TUW	Before commencement of construction activities	Implemented
S3.327 & S3.412	- A monitoring and emergency response plan (to be prepared by the Contractor), in relation to potential impacts due to groundwater drawdown, will form part of the EM&A requirement in the EM&A Manual subject to approval by EPD and AFCD before commencement of the tunnelling and MPV construction in Mai Po area. The plan should include, but not be limited to, details of monitoring locations and programme, a mechanism to monitor the implication from the works to the groundwater system and fish pond, action levels and emergency responses such as immediate action, remedial action and investigation.	To detect potential impacts due to groundwater drawdown	Contractor	MPV	Before commencement of the tunnelling and MPV construction	AFCD's comment has been sought during formulation of Plan

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S3.413	- A monitoring and emergency response plan, in relation to impacts due to noise/vibration, should form part of the EM&A requirement in the EM&A Manual subject to approval by EPD and AFCD before commencement of the tunnelling and MPV construction in Mai Po area.	To detect and monitor noise / vibration impacts	Contractor	MPV	Before commencement of bore tunnelling and MPV construction	Implemented
Ecological Impact (Construction Phase)						
S3.325 - S3.326	- Implementation of precautionary measures during tunnelling works.	To avoid potential hydrogeological impacts	Contractor	All works areas	Construction phase	To be implemented as per construction programme
S3.409 to S3.410	- Ecological impact monitoring focusing on habitats and species of conservation interest should be conducted during the construction phase at the MPV, TPP, SSS / ERS, PHV, and TUW sites where a	To monitor potential indirect construction impacts to wildlife	MTR	MPV, TPP, SSS / ERS, PHV, and TUW	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	number of avifauna of conservation interest (e.g. overwintering bird, Greater Painted-snipe) and areas of conservation interest (e.g. country parks, conservation areas, and wetlands) were recorded. - Avifaunal communities should be surveyed quantitatively along transects. Birds heard or seen along the transects should be identified to species and counted. The nature of construction works within works area conducting during each impact monitoring visit should also be recorded. The quantitative monitoring results should be compared to pre-construction condition. The impact monitoring results should be undertaken by qualified ecologist(s) with relevant working experience. - Should any unpredicted indirect ecological impacts arising from the proposed Project be detected, remedial measures should be developed and implemented by the Contractor.		MTR Contractor			

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S3.327 & S3.412	- Implementation of the groundwater monitoring and emergency response plan.	To detect and minimize hydrological impacts	Contractor	MPV	Construction phase (During bore tunneling works and construction of Mai Po Ventilation Shaft)	Refer to Item for S3.327 & S3.412.
S3.413	- Implementation of monitoring and emergency response plan on noise and vibration.	To detect and minimize noise / vibration impacts	Contractor	MPV	Construction phase (During bore tunneling works and construction of Mai Po Ventilation Shaft)	Implemented
S3.364 -S3.369	- Use of quiet construction plant and temporary noise barriers.	To minimise impacts to surrounding habitats	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	- Access to the ventilation building sites should follow existing access roads, such as the maintenance access along the existing drainage channels. - Site hoarding of about 2.4 m high should be erected around the works area of access roads along drainage channels in the TPP and SSS / ERS sites. - Gate and fences should be installed along the construction accesses that are adjacent to public areas. - Gates and hoardings should be provided at the entrances/exits and along the boundary of the works areas respectively to prevent any trespassers from encroaching or will fully disturbing any wild animals and their habitats within the works areas. - A trip-ticket system should be adopted to monitor the disposal of construction and demolition materials. CCTV and warning signs should be provided at the					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	entrance of the proposed temporary and permanent vehicular access.					
3.370 -3.371 and 3.373	- Vegetation located within the works areas should be preserved as far as practicable. - To avoid soil compaction, heavy machinery should not be used in close proximity to vegetation. Soils that become compacted through the activities of the development should be loosened to an appropriate depth to allow seed germination. - All temporarily affected habitats should be reinstated after the completion of works. - Placement of equipment or stockpiles should be confined to designated works areas. Access routes should be confined on existing disturbed land, where practicable.	To minimize impacts to vegetation	MTR / Contractor	All works areas	Construction phase	Implemented
	- Detailed vegetation survey should be conducted in	To minimize impacts to	MTR /	TSW	Prior to	Vegetation

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	TSW site prior to commencement of site clearance.	vegetation	Contractor		commencement of site clearance	Survey Report formulated and deposited to EPD
	- To mitigate the loss of the vegetation and habitats, planting of native species should be provided in the areas affected by the Project in TSW site, and other works area, where practicable.	To minimize impacts to vegetation	MTR / Contractor	TSW and all other works areas	Construction phase	Proposal of mitigatory planting at TSW was included in the Vegetation Survey Report. Mitigatory planting to be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
						construction programme
S3.372	- The affected individuals of Incense Tree within the NTV works area should be transplanted to nearby suitable habitats prior to the commencement of site clearance at NTV works area as far as practicable. - A detailed vegetation survey covering the affected habitat at NTV works area should be conducted by a suitably qualified botanist / ecologist to identify and record the affected individuals in order to provide details for the transplantation scheme prior to the commencement of site clearance. Feasibility and suitability of transplanting the affected individuals would be studied and suitable receptor sites would be identified. The transplantation proposal for the affected individuals should be prepared as necessary and transplantation should be supervised by a	To minimize impacts to vegetation	MTR / Contractor	NTV	Construction phase	Vegetation survey was conducted and included in the Vegetation Survey Report. Transplantation of Incense Tree was completed and monitored.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	suitably qualified ecologist / horticulturist.					
S3.374 - S3.377	- Site hoarding of 2.4 m high should be set up along the boundary of the works areas as far as practicable.	To minimize disturbance to wildlife	Contractor	All works areas	Construction phase	Implemented
	- The erection of hoarding (2.4 m) along KT5 in the area with high Greater Painted-snipe occurrence (e.g. the proposed access road next to KT5) should avoid their breeding season, prior to construction activities in the area.			KT5 (near TPP)	Prior to the construction of access road	Implemented
	- The use of noisy construction equipment such as hydraulic breakers should be avoided at the area with high painted-snipe occurrence (e.g. the proposed access road next to KT5) during their breeding season as far as practicable.			KT5 (near TPP)	Construction phase	Implemented
	- Hoardings of 2.4 m height should be put in place before commencement of construction activities. Hoarding at the section along the northern boundary			MPV	Right after possession of site	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	of the MPV works area should be installed first. The duration of hoarding erection should be kept as brief as practicable. - Upon the erection of site hoarding, all construction activities should be conducted within the fenced area.					
	- Major construction site lighting should point inward and downward. Unnecessary lighting should be turned off outside working hours of the construction sites.			All works area	Construction phase	Implemented
S3.378 - S3.380	- Excavation works carried out within waterbodies should be carried out in dry season where practicable. - Excavation works within the watercourse / drainage channel should be restricted when possible to an enclosed dry section of the watercourse / drainage channel, with containment measures such as bunds and barriers used within the watercourse / drainage	To minimise pollution to waterbodies	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	channel. - Site runoff should be directed towards regularly cleaned and maintained silt traps and oil / grease separators. The silt and oil / grease separators should be appropriately designed for the local drainage and ground conditions. Tightly sealed closed grab excavators should be deployed where material to be handled is wet. - The flow of the watercourse and drainage channel located with the Project Area should be maintained throughout the construction phase.					
Terrestrial Ecological Impact (Post-construction / Operation Phase)						
S3.327 & S3.412	- Implementation of the groundwater monitoring and emergency response plan.	To detect and minimize hydrogeological impacts	Contractor	MPV	Post-construction phase	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
						programme
S3.381	- The affected agricultural land should be restored to a condition suitable for agricultural use before handing over to landowners / operators.	To minimize impacts to surrounding habitats	MTR / Contractor	All temporarily occupied agricultural land	Operation phase	To be implemented as per construction programme
S3.382 – S3.384	- Vegetation control in the constructed channels should be implemented to prevent the excessive growth of vegetation that would impede the drainage capacity of the channel. To minimise sedimentation, de-silting should be limited to the dry season (November to March). The natural stream bed substrate should not be removed from the channel during de-silting works. - For maintenance de-silting, temporary barrier walls should be used to provide a dewatered zone for de-silting works. Waste material produced during de-silting should be disposed of in a timely and	To minimise impacts to constructed channels	MTR	All constructed channels in SSS	Operation phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	appropriate manner.					
S3.385 & S3.387	- Large areas of reflective material (including glass) should not be used on the outer surfaces of the buildings. - All the major lighting sources should point inward and downward to minimise glare disturbance to wildlife. The intensity of light should also be controlled to the lowest possible level.	To minimise impacts to wildlife	MTR / DDC	All ventilation buildings in northern section and SSS	Detailed design and Operation phases	To be implemented as per construction programme
S3.411	- Implementation of ecological habitat management plan. - Ecological monitoring of the mitigation stream habitats according to ecological habitat management plan.	To monitor the wildlife use of the mitigation stream habitat	MTR	Mitigation stream habitat in SSS / ERS	Operation phase	To be implemented as per construction programme
Marine Ecological Impact (Construction Phase)						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Appendix3.6 (S1.102)	- The use of high-speed vessels should also be avoided during the construction and operation of the proposed barging point.	To minimise the indirect impact to Chinese White Dolphin habitat	Contractor	LKB	Construction phase	To be implemented as per construction programme
Appendix3.6 (S1.103)	- No dumping of rubbish, oil or chemicals would be allowed.	To minimise the pollution to marine habitats	Contractor	LKB	Construction phase	To be implemented as per construction programme
Appendix3.6 (S1.104)	- Deployment of silt curtains around the closed grab dredgers to minimize the suspended sediment impact due to dredging activities in dredging region. - To minimize impact on the gorgonians along the coastline near the dredging area, double silt curtains should be deployed around the works area.	To minimise the impact to subtidal habitats	Contractor	LKB	Construction phase	To be implemented as per construction programme
Appendix3.6	- The number of work vessels and small crafts should be minimized. Dredging should be carried out	To minimise disturbance impact on Chinese White	Contractor	LKB	Construction	To be implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
(S1.106)	continuously without unnecessary break to prevent unpredictable or sudden noise outbursts at random intervals.	Dolphin			phase	as per construction programme
Appendix3.7 (S1.83)	- Mitigation measures to control water quality impacts proposed under Section 11 should be adopted.	To minimise indirect impact to intertidal and subtidal flora and fauna	Contractor	WKT	Construction phase	Implemented
Appendix3.6 (S1.105)	- Engines of vessels moored at the barging point would be turned off to minimize unnecessary underwater noise.	To minimise disturbance impact on Chinese White Dolphin	Contractor	LKB	Construction phase	To be implemented as per construction programme
Pond Fisheries Impact (Pre-construction Phase)						
S4.51	- A monitoring and emergency response plan, in relation to potential impacts due to groundwater drawdown, will form part of the EM&A requirement in the EM&A Manual subject to approval by EPD and AFCD before commencement of the tunnelling	To detect and minimize potential hydrological impacts	Contractor	MPV	Pre-construction phase (Before commencement of the tunnelling and MPV	AFCD's comment has been sought during formulation

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	and MPV construction in Mai Po area. The plan should include, but not be limited to, details of monitoring locations and programme, a mechanism to monitor the implication from the works to the groundwater system and fish ponds including their water levels, action levels and emergency responses such as immediate action, remedial action and investigation.				construction)	of Plan
S4.52	- A monitoring and emergency response plan, in relation to impacts due to noise/vibration, should form part of the EM&A requirement in the EM&A Manual subject to approval by EPD and AFCD before commencement of the tunnelling and MPV construction in Mai Po area.	To detect and monitor noise / vibration impacts	Contractor	MPV	Pre-construction phase (Before commencement of bore tunnelling and MPV construction)	Implemented
S4.45	- Consultation should be conducted with fish operators	Engagement of	Contractor /	MPV	Pre-construction	To be

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	in Mai Po before tunnelling starts. The method of construction, potential impact and mitigation measures should be fully explained to the operators at the meeting.	stakeholders	MTR		phase (Before commencement of tunneling works)	implemented as per construction programme
Pond Fisheries Impact (Construction Phase)						
S4.51	- Implementation of the groundwater monitoring and emergency response plan.	To detect and minimize hydrogeological impacts	Contractor	MPV	Construction phase (During bore tunneling works and construction of Mai Po Ventilation Shaft)	Implemented
S4.52	- Implementation of the monitoring and emergency response plan on noise and vibration.	To detect and minimize noise / vibration impacts	Contractor	MPV	Construction phase (During bore tunneling works and	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
					construction of Mai Po Ventilation Shaft)	
S4.40	- Good site practices and proper dust and water quality control measures should be implemented. These include site confinement with fencing/hoarding erection at the perimeter of the works area, stockpile covering by impervious sheeting to avoid spread of construction dust, and proper handling, storage and disposal of chemical waste to avoid contamination of the existing water system, etc.	To minimize the indirect off-site impacts on the adjacent fishponds	Contractor	MPV	Construction phase	Implemented
S4.44	Implementation of good site practices during the construction phase: ▪ Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;	To minimize disturbance to fishponds by construction noise	Contractor	MPV	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Silencers or mufflers on construction equipment should be utilized and properly maintained during the construction program; ▪ Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; ▪ Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby fishponds; ▪ Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities; ▪ Use of movable barrier for certain powered mechanical equipment (PME); and ▪ Use of noise enclosure or acoustic shed to cover certain stationary PME.					
Pond Fisheries Impact (Post-construction Phase)						
S4.51	- Implementation of the groundwater monitoring and	To detect and minimize	Contractor	MPV	Post-Constructio	To be

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	emergency response plan.	hydrogeological impacts			n phase	implemented as per construction programme
Marine Fisheries Impact (Construction Phase)						
Appendix4.2 (S1.38)	- Mitigation measures to control water quality impacts proposed under Section 11 should be adopted.	To minimize the indirect impact on fisheries resources	Contractor	LKB and WKT	Construction phase	To be implemented as per construction programme
Airborne Noise Impact (Construction Phase)						
S5.120	The following good site practices should be implemented: ▪ Only well-maintained plant should be operated on-site and plants should be serviced regularly during the construction program; ▪ Silencers or mufflers on construction equipment should be utilized and should be properly	To reduce construction noise impact	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	maintained during the construction program; ▪ Mobile plant, if any, should be sited as far from noise sensitive receivers (NSRs) as possible; ▪ Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; ▪ Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and ▪ Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.					
S5.121-S5.122 and Table 5.22	The following quiet PME should be used: ▪ Pneumatic breaker (SWL=110dB(A)) ▪ Tracked Excavator Fitted with Hydraulic Breaker (SWL=110dB(A)) ▪ Truck Mixer (SWL=100dB(A))	To reduce construction noise impact	MTR / Contractor	Works Areas A, B, C, D, E, F, G, H, I, J, K, L, M, N, O, P, Q, R, S, T, U, V, W,	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Tracked Crane (SWL=101dB(A)) ▪ Dump Truck (SWL=103dB(A)) ▪ Tracked Excavator/Loader (SWL=105dB(A)) ▪ Dozer (SWL=111dB(A)) ▪ Road Roller (SWL=101dB(A))			Y, Z, AA, AC, AE, AF, AG and AH		
S5.123 - S5.124	Movable noise barrier should be used for the following PME where practicable: ▪ Mini backhoe ▪ Breaker, mini-robot mounted ▪ Vibratory poker ▪ Handheld breaker ▪ Excavator ▪ Grab ▪ Tracked Crane	To reduce construction noise impact	MTR / Contractor	Works Areas A, C and D	Construction phase	Implemented
S5.125	Noise enclosure/acoustic shed should be used for the following PME where practicable: ▪ Air compressor	To reduce construction noise impact	MTR / Contractor	Works Areas A, B, C, D, E, F, G, H, I, J,	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Concrete pump ▪ Grout pump ▪ Shotcrete pump			K, L, M, O, P, Q, S, T, U, V and Z		
S5.125	Acoustic enclosure should be used for enclosing drilling jumbo as fully as possible.	To reduce construction noise impact	MTR / Contractor	Works Areas B, C, F, H and J	Construction phase	To be implemented as per construction programme
S5.127	Silencer should be used for the ventilation fans.	To reduce construction noise impact	MTR / Contractor	Works Areas A, B, C, D, E, F, H, J, L and P	Construction phase	To be implemented as per construction programme
S5.128	Noise insulating fabric should be applied where practicable to cover the following PME: ▪ Drill rig ▪ Grab and chisel	To reduce construction noise impact	MTR / Contractor	Works Areas A, B, C, D, E, G, L, M, N, O, Q, R, S, V	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Oscillator & casings ▪ Piling rig ▪ Piling, large diameter bored, reverse circulation drill ▪ Piling, vibrating hammer					
S5.130	Use of "Noise Insulating Cover" to cover the mucking out points.	To reduce construction noise impact	MTR / Contractor	Works Area L	Construction phase	To be implemented as per construction programme
S5.131	Use of temporary hoardings along the works boundary.	To reduce construction noise impact	MTR / Contractor	Works Areas B and D	Construction phase	Implemented
S5.134-S5.136	Use of saw instead of mini-robot mounted breaker and oscillator pile for removal of superstructures	To reduce construction noise impact	MTR / Contractor	Works Areas N, O and S	Construction phase	Implemented
S5.137	Scheduling of construction works outside school examination periods	To reduce construction noise impact	MTR / Contractor	Works Areas G, J, K, L, N, O, P, Q, Y, U,	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
				V and AH		
S5.193	Airborne construction noise monitoring should be conducted in accordance with EM&A Manual to monitor the airborne noise impact.	To monitor airborne noise impact	MTR / Contractor	Proposed monitoring locations	Construction phase	Implemented
Airborne Noise Impact (Operation Phase)						
S5.113 and Table 5.21	The maximum permissible sound power levels (Max SWLs) for the fixed plant should be complied with during the selection of equipment and mitigation measures.	To comply with the noise criteria of Noise Control Ordinance	MTR / DDC	MPV, NTV, PHV, SMV, KCV, NCV, MKV, WKV and WKT	Detailed design and operation phases	To be implemented as per construction programme
S5.140	Noise barrier should be erected as follow: ▪ A 8m high barrier along the access road on eastern side of SSS; and ▪ 5.5m barrier along western boundary facing Leung	To comply with the noise criteria of Noise Control Ordinance	MTR / DDC	SSS	Detailed design and operation phases	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	Uk Tsuen squats.					programme
S5.140	Installation of 13m absorptive panels on both sides and full length of ERS.	To comply with the noise criteria of Noise Control Ordinance	MTR / DDC	ERS	Detailed design and operation phases	To be implemented as per construction programme
S5.196	Noise commissioning test is recommended to monitor the ground-borne noise level complying with NCO.	To monitor ground-borne noise impact	MTR / Contractor	Proposed monitoring locations	Operation phase	To be implemented as per construction programme
Ground-borne Noise Impact (Construction Phase)						
S6.82	Ground-borne construction noise monitoring should be conducted in accordance with EM&A Manual to monitor the ground-borne noise impact.	To monitor ground-borne noise impact	MTR / Contractor	Proposed monitoring locations	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S6.85	Construction groundborne noise measurement results should be used to further update the ground-borne noise prediction where appropriate.	To update the predicted ground-borne noise levels.	MTR / Contractor	TBM tunneling section	Construction phase	To be implemented as per construction programme
S6.83	Conduct tests of the FDL of the train to update the ground-borne noise prediction and the recommended mitigation measures as necessary.	To confirm the predicted ground-borne noise levels	MTR	-	Prior to the final design of the trackform and the extent of each type of trackform, and after the proposed train in operation outside Hong Kong	To be implemented as per construction programme
S6.84	Conduct vibration borehole testing at two carefully selected locations along the proposed tunnel alignment	To confirm the predicted ground-borne noise levels	MTR	Proposed two locations	Prior to the commencement	To be implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	to determine the LSR values under certain geological conditions. The ground-borne noise predictions and the recommendation on mitigation measures should be updated as necessary.				of construction works	as per construction programme
Ground-borne Noise Impact (Operation Phase)						
S6.87	Noise commissioning test is recommended to monitor the ground-borne noise level complying with NCO.	To monitor ground-borne noise impact	MTR / Contractor	Proposed monitoring locations	Operation phase	To be implemented as per construction programme
Landscape and Visual Impact (Construction Phase)						
Table 7.10	All existing trees should be carefully protected during construction as far as possible in accordance with ETWB TCW No. 29/2004 and 3/2006.	To minimize landscape and visual impacts during construction phase	Contractor	Works areas	Detailed design and construction phases	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	Trees should be retained on site as far as possible. Should removal of trees be unavoidable due to construction impacts, trees will be transplanted or felled depending on stated criteria in the Tree Removal Applications to be submitted separately in accordance with ETWBC 2/2004 and 3/2006. Wood resulting from tree removal should be recycled as mulch or soil conditioner which could be used within the Project or in other projects as much as possible.		Contractor			
	Control of night-time lighting glare.		Contractor			
	Erection of decorative screen hoarding to screen off undesirable views of the construction site having consideration of safety and security.		Contractor			
	Reuse of existing topsoil where possible for new planting areas within the project.		Contractor			
Landscape and Visual Impact (Operation Phase)						
Table	~~Compensatory tree planting should be incorporated into~~	To minimize landscape	MTR	Works areas	Detailed design	To be

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
7.11	the proposed Project where space is available	and visual impacts during operation phase			and operation phases	implemented as per construction programme
	Landscape and visual enhancement treatments		MTR			
	Compensatory habitat proposal for natural stream course at SSS		MTR			
	Reinstatement of works area in Nam Cheong Park to integrate with the existing park.		MTR			
	Tall buffer tree planting should be incorporated provide screening to ventilation buildings, engineering structures and associated facilities.		MTR			
	Roof greening to mitigate the visual impact of VB on the VSRs at high level.		MTR			
	Vertical greening would be incorporated where practicable to visually soften the façade of ventilation building and/or noise barrier		MTR			
	Incorporation of aesthetically pleasing streetscape design which would be responsive to adjacent landscape context.		MTR			

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	Roadside amenity trees to enhance the landscape and visual quality of the existing and proposed road.		MTR			
	Reinstatement of disturbed areas to match adjacent area or to condition to suit future landuse.		MTR			
	Aesthetically pleasing design as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities so as to blend in the buildings and structures to the adjacent landscape and visual context.		MTR			
	Control of Operation Night-time Glare		MTR			
	Incorporation of aesthetically pleasing design to boundary fence so as to blend in the structure to the adjacent landscape and visual context.		MTR			
	The scale, location, disposition and design of the ventilation shafts at WKCD would be further reviewed and submitted to relevant parties (e.g. WKCDA and PlanD) for agreement.		MTR			

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Cultural Heritage Impact						
S8.100 – S8.103	• Conduct further investigation (a minimum of 18 trial pits, 1m x 1.5m) to confirm any archaeological remains exist in the inaccessible areas (**NOL/ERL/300/C/XRL/ENS/M55/303- 304 & 306-307**). If archaeological data collected from these 18 test pits is insufficient to ascertain the archaeological potential of the inaccessible areas, additional test pits should be conducted • Conduct rescue excavation to preserve	To confirm any archaeological remains exist in the inaccessible areas and to preserve archaeological remains if any	MTR	Proposed rescue excavation area in SSS and other archaeological deposit areas identified in the further	Prior to construction phase	Further Archaeological Investigation has been conducting according to Archaeological Action

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	archaeological remains by detailed records if found (**NOL/ERL/300/C/XRL/ENS/M55/307**)			archaeological investigation		Plan formulated
S8.103	Conduct archaeological watching brief during construction works at TUW for identification of any historical finds during construction phase	To identify any historical finds in the works area	MTR	TUW	Construction phase	To be implemented as per Archaeological Action Plan formulated
S8.104	Conduct regular site audit during the construction of barging point to confirm that no excavation works is conducted at Lung Kwu Sheung Tan archaeological deposit area.	To avoid direct impact	MTR	LKST barging point and associated access road	Construction phase	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
						programme
S8.105	Restriction of works boundary of TPP to be extended to relics discovered area outside TPP.	To avoid direct impact	MTR	TPP	Construction phase	Implemented
S8.107, S8.128	Avoid works areas at the sites of the identified built heritage structures as far as practicable. Identified earth shines within works boundary of SSS and TPP will be relocated by local villagers prior to commencement of construction works at SSS and TPP.	To avoid direct impact	MTR	Earth shines (NHL-04,TKP-02 and LET-07)	Prior to construction phase	Implemented
S8.109, S8.125	Vibration monitoring at Lai Chi Kok Hospital: ▪ Prior to commencement of construction works, the location and installation of the monitoring stations should be discussed and agreed with AMO, Hong Kong Institution for Promotion of Chinese Culture (the "NPO", selected organization for the Revitalisation Scheme), the Commissioner for Heritage's Office and relevant parties before installation. ▪ Compliance monitoring of vibration limits should be	To monitor vibration impacts on the identified vibration sensitive historical buildings	MTR	Ex-Lai Chi Kok Hospital	Before construction phase; Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	conducted and reported as a requirement of EM&A programme.					
S8.110, S8.126	▪ A further condition survey and appropriate consolidation works (e.g. installation of temporary propping or reinforced timber beam to maintain the stability of structure etc.), if required, will be carried out on Blocks P Q, W and the inaccessible area of LCKH prior to construction. It should be discussed and agreed in advance with AMO, NPO, the Commissioner for Heritage's Office and relevant parties,	To minimize vibration impacts on the identified vibration sensitive historical buildings	MTR	Ex-Lai Chi Kok Hospital	Detailed design	To be implemented as per construction programme
S8.112, S8.127	▪ If consent is given by the property owner, a condition survey will be carried out at Cheung Yuen prior to the commencement of works in SSS. The survey should be discussed and agreed in advance with AMO and property owner prior to commencement of survey.	To minimize vibration impacts on the identified vibration sensitive historical buildings	MTR	Cheung Yuen	Prior to construction phase	AMO's comment has been sought during formulation of Vibration Monitoring

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
						Plan
S8.112, S8.127	▪ If consent is given by the property owner, vibration monitoring at LET-06 (Cheung Yuen) will be conducted when excavation works are being conducted within 50m radius from the house. The monitoring location should be discussed and agreed with AMO and property owner before installation.	To monitor vibration impacts on the identified vibration sensitive historical buildings	MTR	Cheung Yuen	Construction phase	To be implemented as per construction programme
S8.113, S8.124	▪ Control of vibration levels from the proposed blasting and excavation activities within a peak particle velocity (ppv) limit of 25mm/s to prevent potential vibration impact to all identified built heritage resources.	To minimize vibration impacts on the identified vibration sensitive historical buildings	MTR	All works area where blasting and excavation activities are involved	Construction phase	To be implemented as per construction programme
S8.114 - S8.115	▪ Use of sensibly designed screen hoardings for reducing the potential visual impact.	To minimize visual impacts	MTR	All identified heritage buildings in	Detailed design and construction phase	To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
				all works areas		construction programme
Land Contamination Impact						
S9.28 – S9.33	Remediation of Contaminated Soil ▪ After excavation, confirmation sampling and testing shall be conducted from the sidewalls and at base of the excavations to ensure complete excavation of contaminated soils. ▪ Bioremediation (biopiling) / ex-situ chemical oxidation are proposed to remediate the contaminated soil recorded in Sites H and Q. Remediation Report(s) (RR) for contaminated works area(s) should be prepared by the Land Contamination Specialist to detail the remediation process and demonstrate that contaminated soils are all removed, properly handled and disposal of. The remediated soil should be reused on site to minimise the waste disposal.	To remediate contaminated soil	Contractor	Sites H and Q	Site remediation	For Site H: Remediation has been conducting according to the approved Supplementary RAP. For Site Q: To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S9.35(i)	For construction works of the alignment close to Ngau Tam Mei Landfill ▪ As a general precautionary measure, visual inspection of excavated materials should be conducted to screen soil for signs of contamination (e.g. discoloration, stains and odour). The inspection process should also be assisted by a photo ionization detector (PID) for volatile organics. If suspected materials are encountered during tunnel boring, sampling and testing for the parameters recommended in Table 6.1 of CAP should be undertaken to verify any contamination. The suspected soil bored out during excavation and tunnel boring should be temporary stockpiled and if laboratory analysis indicated exceedance of relevant RBRG levels, remediation works, should be undertaken depending on the quantity and quality of contaminated soil identified.	Acting as a general precautionary measure to screen soil for signs of contamination during tunnel boring works under/close to Ngau Tam Mei Landfill	MTR/Contractor	Within the Landfill Boundary where signs of contamination is identified	During Tunnel Boring within Ngau Tam Mei Landfill Boundary Section	To be implemented as per construction programme
S9.35(ii)	For construction works at CLP transformer station at Lai Cheung Road and Petrol Filling Station at 82 Tai Kok Tsui Road ▪ As a general precautionary measure, visual	Acting as a general precautionary measure to screen soil for signs of contamination during	MTR/Contractor	Area close to CLP transformer station at Lai	During Tunnel Boring/ excavation works near CLP	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	inspection of excavated materials should be conducted to screen soil for signs of contamination (e.g. discoloration, stains and odour). The inspection process should also be assisted by a photo ionization detector (PID) for volatile organics. If suspected materials are encountered during tunnel boring, further sampling and testing should also be undertaken to verify any contamination. The soil bored out during excavation and tunnel boring should be temporary stockpiled and if laboratory analysis indicated exceedance of relevant RBRG levels, remediation works, should be undertaken depending on the quantity and quality of contaminated soil identified.	tunnel boring/ excavation at CLP transformer station at Lai Cheung Road and Petrol Filling Station at 82 Tai Kok Tsui Road		Cheung Road and Petrol Filling Station at 82 Tai Kok Tsui Road where signs of contamination is identified	transformer station at Lai Cheung Road and Petrol Filling Station at 82 Tai Kok Tsui Road	programme
S9.35 (iii)	For sites with contamination identified (Site H and Site Q) the following environmental mitigation measures should be undertaken during the course of the site remediation: ▪ Excavation profiles must be properly designed and executed with attention to the relevant requirements for environment, health and safety; ▪ Excavation should be carried out during dry season as far as possible to minimise contaminated runoff	To minimise the potentially adverse environmental impacts arising from the handling of potentially contaminated materials.	Contractor	Sites H and Q /during transportation	Site remediation and prior to construction phase	For Site H: Implemented For Site Q: To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	from contaminated soils; ▪ Supply of suitable clean backfill material is needed after excavation; ▪ The chemical oxidant proposed (RegenOxTM) as a contaminant mass reduction technology. Comprises a solid oxidant complex (sodium percarbonate/catalytic formulation) and an activator complex (a composition of ferrous salt embedded in a micro-scale catalyst gel). These chemical will be securely stored, separately and way from sources of ignition or oxidizable items. Handling will & will be undertaken by persons specifically trained and wearing appropriate PPE. ▪ Vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates should be sealed to prevent any discharge during transport or during wet conditions; ▪ Speed control for the trucks carrying contaminated materials should be enforced; and ▪ Vehicle wheel and body washing facilities at the site's exist points should be established and used.					construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S9.35(iv)	In order to minimise the potentially adverse effects on health and safety of construction workers during the course of site remediation, the Occupation Safety and Health Ordinance (OSHO) (Chapter 509) and its subsidiary Regulations should be followed by all site personnel working on the site at all times. In addition, the following basic health and safety measures should be implemented as far as possible: ▪ Set up a list of safety measures for site workers; ▪ Provide written information and training on safety for site workers; ▪ Keep a log-book and plan showing the contaminated zones and clean zones; ▪ Maintain a hygienic working environment; ▪ Avoid dust generation; ▪ Provide face and respiratory protection gear to site workers; ▪ Provide personal protective clothing (e.g. chemical resistant jackboot, liquid tight gloves) to site	To minimise the potentially adverse effects on health and safety of construction workers during the course of site remediation	Contractor	Sites H and Q	Site remediation and prior to construction phase	

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	workers; and ▪ Provide first aid training and materials to site workers.					
9.35(v)	For Areas Feasible or Infeasible for On-Site Inspection and Site Investigation (i) Phase 2 supplementary SI works ▪ Upon site access is granted, site inspection should be carried out to ascertain any contaminative sources and hotspot of contamination within the site. ▪ The sampling and testing schedule as recommended in the approved CAP should then be updated based on respective site situation and the number of sampling locations may be significantly reduced. A revised CAP should then be submitted to EPD for endorsement. ▪ For supplementary CARs and RAP(s), upon completion of SI and laboratory testing, supplementary CARs should be submitted to EPD for endorsement. If contamination is identified, RAP(s) should also be submitted to EPD for	(i) To identify areas with land contamination concern, report laboratory results and propose remediation measures if necessary. (ii) To ensure remediation works have been undertaken to before the commencement of any construction works of the Project that may disturb the ground of the south-western portion of the MPV.	MTR/ Contractor	Areas Infeasible for On-Site Inspection and Site Investigation and WSW	After land resumption and prior to the construction works commencement at respective sites	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	endorsement. ▪ The revised CAPs and supplementary CARs and /or RAP(s) should be submitted in separate packages for different works area depending on the schedule of land resumption and the commencement of construction works for each works area. ▪ RR(s) should be submitted to demonstrate completion of remediation works before construction work starts at the site. (ii) WSW ▪ According to WSW EP Condition 3.14, the Project Proponent of the WSW development shall prepare and submit CAR/RAP to EPD within 2 months after commencement of construction of the WSW development and the recommendations in the endorsed CAR/RAP shall be fully implemented before the commencement of any construction works that may disturb the ground of the relevant sites. ▪ This project will ensure that the completion of remediation works before the construction works at contaminated areas start.					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Waste Management Implications (Construction Phase)						
S10.107	Recommendations for good site practices: ▪ Prepare a Waste Management Plan approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites; ▪ Training of site personnel in, site cleanliness, proper waste management and chemical handling procedures; ▪ Provision of sufficient waste disposal points and regular collection of waste; ▪ Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; ▪ Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and ▪ Separation of chemical wastes for special handling and appropriate treatment.	To implement good site practice for handling, sorting reuse and recycling of C&D materials	Contractor	All works areas	Construction phase	Implemented
S10.108	Recommendations for waste reduction measures: ▪ Sorting of demolition debris and excavated materials from demolition works to recover reusable/ recyclable portions (i.e. soil, broken	To implement on-site sorting facilitating reuse and recycling of materials as well as proper disposal	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	concrete, metal etc.); ▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; ▪ Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the workforce; ▪ Proper storage and site practices to minimize the potential for damage or contamination of construction materials; ▪ Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; and ▪ Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycle.	of waste				
S10.109	The Contractor should prepare and implement a Waste Management Plan (WMP) as a part of the Environmental Management Plan (EMP) in accordance	To keep trace of the generation, minimization, reuse and disposal of	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	with ETWB TCW No. 19/2005 which describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities.	C&D materials in the Project				
S10.112	Storage of materials on site may induce adverse environmental impacts if not properly managed, recommendations to minimise the impacts include: ▪ Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimising the potential of pollution; ▪ Maintain and clean storage areas routinely; ▪ Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and ▪ Different locations should be designated to stockpile each material to enhance reuse.	To minimise potential impacts of waste storage and enhance reusable volume	Contractor	All work areas	Construction phase	Implemented
S10.113	Waste hauliers must hold a valid permit for the collection of waste as stipulated in their permits. Removal of waste should be done in a timely manner.	To collect and remove waste generated	Contractor	All work areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S10.114-115	Implementation of trip-ticket system to monitor waste disposal and control fly-tipping. Set up warning signs at vehicular access points reminding drivers of designated disposal sites and penalties of an offence. Installation of close-circuited television at access points of vehicles to monitor and prevent illegal dumping.	To monitor disposal of waste and control fly-tipping	Contractor	All work areas	Construction phase	Implemented
S10.117	Recommendations for excavated materials within works areas: ▪ Several ramps should be used for transportation of different materials as far as practicable (at SSS/ERS site, both soft and hard materials could be generated with the provision of three ramps, each of them can be used for single material for primary separation). Each ramp should be used for transportation of a single material as far as practicable. ▪ If a conveyor system is used, materials should be transported separately on the belts, it is therefore proposed that more than one conveyor belt should be installed if possible. If more than one material is needed to be transported on a single belt, each	To mitigate and minimize the potential impacts from the storage and transportation of materials within works areas	Contractor	All works areas	Construction Phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	material should be stockpiled separately once they are removed from the excavation face to the ground and the belt should operate at different times with different materials as far as practicable. ▪ Enclosure should also be provided for the conveyor belt, as far as practicable to minimize the of dust generation. ▪ Different locations should be designated for each material during stockpiling. Stockpiling may be needed when the conveyor system is under constraint or when the spoil could not be transported away from works area immediately after excavation. Cover should be provided to dusty stockpiles to avoid the materials from being wind-blown or flushed away by water. It is expected that water spraying system should also be equipped to moisten the materials.					
S10.119	Wet spoil generated from TBM construction, construction of bored piles and D-wall should be properly handled before disposal to Taishan and Fill Banks respectively for reuse in other projects. Dry materials should be mixed with the wet spoil or by the use of lime to reduce water content where applicable.	To minimise impacts to disposal outlet from reception of wet spoil	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S10.120	Wheelwash facilities should be provided before the trucks leave the works area.	To minimise dust impact	Contractor	All works areas	Construction phase	Implemented
S10.121	The Contractor should ensure the on-site separation from inert portion. The waste delivered to landfill should not contain any free water or have water content more than 70% by weight. The haulier must ensure suitable amount of waste would be loaded on different types of trucks used. A one-week notice should be given to EPD with information on Contractor's name and respective contact details.	To meet the requirement for disposal at landfill	Contractor and Waste haulier	All works areas	Construction phase	Implemented
S10.125	This will generally follow the PNAP 25 in handling of dredged/excavated sediment. The dredged / excavated sediments would be loaded onto barges and transported to existing designated disposal sites allocated by the MFC according to their levels of contamination, as presented below: ▪ For Type 1 sediment, the sediments will be excavated/dredged and transport to designated CEDD Facilities, typically at South Cheung Chau and/or Ninepin. ▪ For Type 2 sediment, the sediments will be dredged/excavated and transport to designated	To dispose sediment in an authorized and least impacted way	Contractor	All works areas with sediments concern	Detailed Design and Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	CEDD Facilities, typically at East Sha Chau for confined marine disposal. ▪ For Type 3 sediment, it would require special treatment/disposal before confined marine disposal at CEDD Facilities, typically at East Sha Chau. In order to have the least potential of loss of contaminants to the marine environment, containment of the sediments in geosynthetic containers is proposed when transporting the sediment. Field trials are recommended to be undertaken during the detailed design stage to establish the optimum handling method for this approach. The details of the disposal methodology could therefore be confirmed during the detailed design stage, prior to construction.					
S10.126	The basic requirements and procedures for dredged / excavated sediment disposal specified under PNAP 252 shall be followed.	To dispose sediment in an authorized and least impacted way	Contractor	All works areas with sediments concern	Construction phase	Implemented
S10.127	The Project Proponent will agree in advance with MFC of CEDD on the site allocation by submitting a Construction & Demolition Material Management Plan. The final disposal sites and arrangement will be	To determine the best handling and disposal option of the sediments.	MTR/ Contractor	All works areas with sediments concern	Detailed Design and Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	determined by the MFC and a dumping permit will be obtained from the DEP prior to the commencement of the dredging and excavation works.					
S10.128	The contractor for the dredging/ excavation works shall apply for the site allocations of marine sediment disposal based on the prior agreement with MFC/CEDD. The contractor shall apply for all necessary permits from relevant authorities for the disposal of dredged / excavated sediment.	To dispose the sediments in an authorized way.	Contractor	All works areas with sediments concern	Construction phase	Implemented
S10.129	If temporary stockpiling of sediments is necessary, the sediment should be covered by tarpaulin and earth bunds or sand bag barriers should be provided on site to prevent leachate from entering the drains and surrounding water bodies. The stockpiling areas should be completely paved or covered by lining avoiding contaminating the soil or groundwater underneath.	To prevent the cross contamination of surrounding soils and water bodies	Contractor	All works areas with sediments concern	Construction phase	Implemented
S10.130	The dredged / excavated sediment should be transported by covering trucks to designated barging points. The barge transporting the sediments to the designated disposal site should be equipped with tight fitting seals to prevent leakage. Besides, the barge should not be filled to a level that would cause overflow of materials or laden water during loading or transportation.	To prevent overflowing of sediments to the surrounding area and water bodies	Contractor	All works areas with sediments concern / trucks / barges	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S10.131	Loading of the dredged / excavated sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water.	To prevent overflowing of sediments to the surrounding area and water bodies	Contractor	Barging points	Construction phase	Implemented
S10.132	In order to minimise the potential odour emissions during the dredging / excavation operation and transportation of the sediment, the dredged / excavated sediment placed on barges should be properly covered as far as practicable. Requirement of the *Air Pollution Ordinance (Construction Dust) Regulation*, where relevant, should be adhered to during the construction phase of the Project.	To minimise dust and odor impacts to surrounding environment	Contractor	All works areas with sediments concern / Barging points	Construction phase	Implemented
S10.134	Workers should wear protective gloves when carrying out the dredging / excavation works. Adequate washing and cleaning facilities should be provided on site.	To minimise the exposure to the contaminated sediments	Contractor	All works areas with sediments concern	Construction phase	Implemented
S10.135	For allocation of sediment disposal site and application of marine dumping permit, another proposal for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval following the procedures in PNAP 252. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging/excavation activities to confirm the sediment	To analyse the sediments quality and determine the best disposal option	Contractor	All works areas with sediments concern	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	disposal method. The contamination levels of the marine sediment to be dredged / excavated have to be analysed and recorded. After carrying out the sampling and testing, a Sediment Quality Report (SQR) will be prepared for EPD approval as required under the *Dumping at Sea Ordinance* to agree and confirm the quantities and extent of the contamination of the sediments prior to the dredging/ construction contract being tendered. The SQR will include the sampling details, the chemical testing results, quality control records, proposed classification and delineation of sediment according to the requirements of the Appendix A of PNAP 252.					
S10.136	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the *Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes*. Containers used for storage of chemical waste should : ▪ Be compatible with the chemical wastes being stored, maintained in good condition and securely sealed; ▪ Have a capacity of less than 450 litres unless the specifications have been approved by EPD; and	To properly store the chemical waste within works areas	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the *Waste Disposal (Chemical Waste) (General) Regulation*.					
S10.137	The chemical storage areas should: ▪ Be clearly labelled to indicate corresponding chemical characteristics of the chemical waste and used for storage of chemical waste only; ▪ Be enclosed on at least 3 sides; ▪ Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; ▪ Have adequate ventilation; ▪ Be covered to prevent rainfall from entering; and ▪ Be properly arranged so that incompatible materials are adequately separated.	To prepare appropriate storage areas for chemical waste at works areas	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S10.138	Lubricants, waste oils and other chemical wastes would be generated during the maintenance of vehicles and mechanical equipments. Used lubricants should be collected and stored in individual containers which are fully labelled in English and Chinese and stored in a designated secure place.	To clearly label the chemical waste at works areas	Contractor	All works areas	Construction phase	Implemented
S10.139	A trip-ticket system should be operated in accordance with the *Waste Disposal (Chemical Waste) (General) Regulation* to monitor all movements of chemical waste. The Contractor should employ a licensed collector to transport and dispose of the chemical wastes, to either the approved CWTC at Tsing Yi, or another licensed facility, in accordance with the *Waste Disposal (Chemical Waste) (General) Regulation*.	To monitor the generation, reuse and disposal of chemical waste	Contractor	All works areas	Construction phase	Implemented
S10.140	General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes.	To properly store and separate from other C&D materials for subsequent collection and disposal	Contractor	All works areas	Construction phase	Implemented
S10.141	The recyclable component of general refuse, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of	To facilitate recycling of recyclable portions of refuse	Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.					
S10.142	The Contractor should carry out a training programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins should also be provided in the sites as reminders.	To raise workers' awareness on recycling issue	Contractor	All works areas	Construction phase	Implemented
Waste Management Implications (Operation Phase)						
S10.146-10.147	Chemical waste: ▪ The requirements stipulated in the *Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes* should be followed in handling of chemical waste as in construction phase. ▪ A trip-ticket system should be operated in accordance with the *Waste* Disposal *(Chemical Waste) (General) Regulation* to monitor all movements of chemical wastes which would be	To avoid environmental impacts in handling, storage and disposal of chemical waste	MTR	Ventilation buildings, SSS and WKT	Operation phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	collected by a licensed collector to a licensed facility for final treatment and disposal. ▪ The recommendations proposed for the mitigation of impacts from chemical waste in construction phase should also be followed (refer to S10.104-S10.106).					
S10.148-S10.149	General refuse: ▪ Provide recycling bins at designated areas for proper recycling of papers, aluminium cans and plastics bottles. ▪ Separation from other waste types and collected by licensed collectors at daily basis to minimize the potential impacts from odour and vermin.	To separate general refuse from other waste types and proper disposal of the refuse	MTR	Ventilation buildings, SSS and WKT	Operation phase	To be implemented as per construction programme
S10.150	Industrial waste: ▪ Separation of reusable components like steel before collection by licensed collector	To recycle useful materials from industrial waste and proper disposal	MTR	Ventilation buildings, SSS and WKT	Operation phase	To be implemented as per construction programme
Water Quality Impact (Construction Phase)						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S11.128 - S11.153	Construction site run-off and general construction activities: ▪ The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.	To control water quality impact from construction site runoff and general construction activities	MTR / Contractor	All works areas	Construction phase	Implemented
S11.154	Groundwater seepages from uncontaminated area: ▪ In case seepage of uncontaminated groundwater occurs, groundwater should be pumped out from the works areas and discharged into the storm system via silt removal facilities. Uncontaminated groundwater from dewatering process should also be discharged into the storm system via silt traps.	To control water quality impact from groundwater from uncontaminated area	MTR / Contractor	All works areas	Construction phase	Implemented
S11.155	As the proposed WKT is near the Victoria Harbour, high ground water level regime due to both tidal effects and rainwater infiltration is anticipated. A cofferdam wall should be built to limit groundwater inflow to the excavation works areas in the WKT site.	To control water quality impact from groundwater from uncontaminated area	MTR / Contractor	WKT	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S11.156	To monitor the tide and groundwater relationship, it is recommended to install groundwater level loggers at the nearest tidal areas (i.e. near Mai Po).	To monitor the groundwater level	MTR / Contractor	Mai Po	Construction phase	Implemented
S11.157 - S11.158	Site Runoff or Groundwater from contaminated areas: ▪ No directly discharge of groundwater from contaminated areas should be adopted. ▪ Prior to any excavation works within the potentially contaminated areas, the baseline groundwater quality in the areas should be reviewed based on the past relevant site investigation data and any additional groundwater quality measurements to be performed with reference to *Guidance Note for Contaminated Land Assessment and Remediation* and the review results should be submitted to EPD for examination. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, this contaminated groundwater should be either properly treated or properly recharged into the ground in compliance with the requirements of the TM-DSS. ▪ If wastewater treatment is to be deployed for	To control water quality impact from contaminated groundwater	MTR / Contractor	Excavation areas where contaminated ground-water is found	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	treating the contaminated groundwater, the wastewater treatment unit shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as TPH) to an undetectable range. ▪ All treated effluent from the wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. ▪ If deployment of wastewater treatment is not feasible for handling the contaminated groundwater, groundwater recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in section 2.3 of the TM-DSS. The baseline groundwater quality should be determined prior to the selection of the recharge wells, and submit a working plan to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	recharge well. Groundwater monitoring wells should be installed near the recharge points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater.					
S11.128 - S11.136, S11.160	Barging points: Mitigation measures for control water quality impact from surface run-off should be applied. The following good site practices should also be adopted: ▪ all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash	To control water quality impact from barging point	MTR / Contractor	All barging Points	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ all hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material ▪ construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site ▪ loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation					
S11.161	Effluent discharge: There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality should meet the requirements specified in the discharge licence. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing seawater intakes. If monitoring of the treated effluent quality from the works areas is required during the construction phase	To control water quality impact from effluent discharge from construction site	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD.					
S11.162	Accidental spillage of chemicals: Contractor should register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes**.**	To control water quality impact from accidental chemical spillage	MTR / Contractor	All works areas	Construction phase	Implemented
S11.163	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	To control water quality impact from accidental chemical spillage	MTR / Contractor	All works areas	Construction phase	To be implemented as per construction programme
S11.164	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste	To control water quality impact from accidental chemical spillage	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: ▪ Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. ▪ Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. ▪ Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.					
S11.165	Surface construction works at or in close proximity of watercourses or seafront: ▪ The proposed surface construction works should be carried out in dry season as far as practicable where the flow in the river channel or stream is low. ▪ The use of less or smaller construction plants may be specified to reduce the disturbance to the riverbed or pond deposits.	To control water quality impact from construction works at or in close proximity of watercourses or seafront	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Temporary sewerage system should be designed to prevent wastewater from entering the river, streams and sea. ▪ Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works. ▪ Stockpiling of construction materials and dusty materials should be covered and located away from any water courses. ▪ Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers. ▪ Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable. ▪ Mitigation measures to control site run-off from entering the nearby water environment should be implemented to minimize water quality impacts. Surface channels should be provided along the edge					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	of the waterfront within the work sites to intercept the run-off. ▪ Construction effluent, site run-off and sewage should be properly collected and/or treated. ▪ Any works site inside the water courses should be temporarily isolated. The water flow should be temporarily diverted to downstream by using PVC pipes, steel arrays in concrete case or similar, restricting the excavation works to be conducted within an enclosed dry section of the channel. This works arrangement would provide a dry zone for excavation works within the river channel and would prevent the conveyance of suspended sediment downstream. Dewatering at works section should be conducted prior to the commencement of works. Further limiting or reducing the works area inside the water courses should be considered during wet season or rainstorm event in order to reduce the area of exposed surface. ▪ Silt curtain should be installed around the construction activities at or near the watercourses to minimize the potential impacts due to accidental					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	spillage of construction wastes and excavated materials. ▪ Proper shoring may need to be erected in order to prevent soil or mud from slipping into the watercourses. ▪ Supervisory staff should be assigned to station on site to closely supervise and monitor the works.					
S11.166	Surface construction works close to water gathering grounds: ▪ The conditions as specified in WSD guidelines on protection of Water Gathering Ground should be followed or observed where practicable	To control water quality impact from surface construction works close to Water Gathering Ground	MTR / Contractor	Works areas close to water gathering ground	Construction phase	To be implemented as per construction programme
S11.167	Dredging of marine sediments at LKST: ▪ Closed grab dredger should be used to minimize the loss of sediment during the raising of the loaded grabs through the water column. ▪ No more than one closed grab dredger should be operated at any one time. ▪ Double silt curtains should be deployed around the dredging operations as far as practicable.	To minimize the loss of fine sediment to suspension during dredging of marine sediments at LKST	MTR / Contractor	Marine dredging at LKST	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ The descent speed of grabs should be controlled to minimize the seabed impact speed. ▪ Barges should be loaded carefully to avoid splashing of material. ▪ All barges used for the transport of dredged materials should be fitted with tight bottom seals in order to prevent leakage of material during loading and transport. ▪ All barges should be filled to a level which ensures that material does not spill over during loading and transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.					
S11.83 and S11.165	Diversion of watercourse: ▪ The excavation works at the existing stream in Shek Kong/ Kam Tin Nullah should be carried out by approved methods by the Engineer to minimise erosion. Should excavation works be carried out at the designated section of water course, temporary river diversion should be conducted prior to the commencement of works to avoid water flowing into works area. The temporary diversion of water	To control water quality impact due to diversion of watercourse	MTR / Contractor	Watercourse to be diverted in Shek Kong	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	flow should be performed by appropriate means, such as completing the construction of the proposed channel section for carrying diverted flow prior to excavation works, or other similar methods, as approved by the Engineer to suit the works condition. This works arrangement would provide a dry zone for excavation works within the river channel and would prevent the conveyance of suspended sediment downstream. Dewatering at works section should also be conducted prior to the commencement of works. ▪ Mitigation measures for minimizing the water quality impact for surface construction works at or close to the watercourses should also be applied.					
S. 11.169 - 11.173	Hydrogeological Impact: For the cut and cover tunnels and associated excavations for vent buildings and emergency access/escape points, the following measures should be in place in order to mitigate any drawdown effects to the groundwater table during the operation of the temporary dewatering works: ▪ Toe grouting should be applied beneath the toe level of the temporary/permanent cofferdam walls	To control groundwater hydrogeological impact and groundwater drawdown	MTR/ Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	as necessary to lengthen the effective flow path of groundwater from outside and thus control the amount of water inflow to the excavation. ▪ Recharge wells should be installed as necessary outside the excavation areas. Water pumped from the excavation areas should be recharge back into the ground. The bored tunnels should be constructed using a closed face tunnel boring machine to limit water inflow into the excavation face. The cutter head for the machine will be sealed during excavation and therefore the water inflow from the face will be very small. Precast undrained linings should be installed and back grouted behind the tunnel boring machine as it advances along the alignment to minimize the potential inflow of water behind the cutter head. The Contractor should initially adopt suitable water control strategies while undertaking the excavation works. The water control strategies are shown as follow:					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Probing Ahead: As normal practice, the Contractor will undertake rigorous probing of the ground ahead of tunnel excavation works to identify zones of significant water inflow. The probe drilling results will be evaluated to determine specific grouting requirements in line with the tunnel advance. In such zones of significant water inflow that could occur as a result of discrete, permeable features, the intent would be to reduce overall inflow by means of cut-off grouting executed ahead of the tunnel advance. ▪ Pre-grouting: Where water inflow quantities are excessive, pre-grouting will be required to reduce the water inflow into the tunnel. The pre-grouting will be achieved via a systematic and carefully specified protocol of grouting. ▪ In principle, the grout pre-treatment would be designed on the basis of probe hole drilling ahead of the tunnel face. In the event of excessive drawdown being observed within the ground water table as a result of the tunnelling works even after incorporation of the water					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	control strategies, post-grouting will be applied as described below: ▪ Post-grouting: Groundwater drawdown will be most likely due to inflows of water into the tunnel that have not been sufficiently controlled by the pre-grouting measures. Where this occurs post grouting will be undertaken before the lining is cast. Whilst unlikely to be required in significant measure, such a contingency should be allowed for reduction in permeability of the tunnel surround (by grouting) to limit inflow to acceptable levels. A detailed groundwater monitoring programme should be developed in detailed design stage to monitor both the proposed works and the impact of those works on the adjacent area.					
Water Quality Impact (Operation Phase)						
S11.174	Tunnel run-off and drainage: ▪ Track drainage channels discharge should pass through oil/grit interceptors/chambers to remove	To control runoff from rail track	MTR / DDC	Tunnels and rail tracks	Operation phase	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	oil, grease and sediment before being pumped to the foul sewer/holding tank for further disposal. ▪ The silt traps and oil interceptors should be cleaned and maintained regularly. ▪ Oily contents of the oil interceptors should be transferred to an appropriate disposal facility, or to be collected for reuse, if possible.					programme
S11.175 – S11.176	Sewage effluents: ▪ Connection of domestic sewage generated from the Project should be diverted to the foul sewer wherever possible. If public sewer system is not available, sewage tanking away services or on-site sewage treatment facilities should be provided to prevent direct discharge of sewage to the nearby storm system and all the discharge should comply with the requirements stipulated in the TM-DSS. ▪ For handling, treatment and disposal of other operation stage effluent, the practices outlined in ProPECC PN 5/93 should be adopted where applicable.	To control water quality impact from sewage effluent discharge ventilation buildings, SSS and WKT	MTR / DDC	Ventilation buildings, SSS and WKT	Operation phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S11.177-S11.181	Shek Kong Stabling Sidings (SSS): ▪ All the maintenance areas within the SSS should be housed or covered to prevent generation of contaminated rainwater runoff. All wastewater generated from the maintenance and cleaning activities should be collected and diverted to oil interceptor or other appropriate treatment facilities for proper treatment so that it satisfies the requirements stipulated in the TM-DSS. ▪ In case there is no pubic sewer available for the SSS during the operation phase, all wastewater generated or collected in the SSS should be tankered away for proper disposal to prevent direct discharge of any wastewater to the nearby surface water system. ▪ Oil interceptors should be regularly inspected and cleaned to avoid wash-out of oil during storm conditions. A bypass would be provided to avoid overload of the interceptor's capacity. ▪ All waste oils and fuels should be collected and handled in compliance with the Waste Disposal Ordinance. Site drainage should be well maintained and good management practices should be observed	To control water quality impacts from the operation of Shek Kong Stabling Sidings	MTR/DDC	SSS	Operation phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	to ensure that oils and chemicals are managed, stored and handled properly and do not enter the nearby water streams. Areas for chemical storage should be securely locked. The storage area should have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest, to minimize the impacts from any potential accidents. In case of the occurrence of accidental spillage of chemicals, it is required to take immediate actions to control the release of chemicals. ▪ Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.					
S11.182	For any future maintenance desilting of the newly constructed or diverted watercourses, temporary barrier walls should be used to provide a dry zone for desilting work. Maintenance desilting should be carried out	To control water quality impact due to maintenance desilting of the newly	MTR	Diverted watercourses in Shek Kong	Operation phase	To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	during periods of low flow in the dry season.	constructed or diverted watercourses				construction programme
Air Quality (Construction Phase)						
S 12.78	For concrete batching plant, the requirements and mitigation measures stipulated in the *Guidance Note on the Best Practicable Means for Cement Works (Concrete Batching Plant) BPM 3/2(93)* should be followed and implemented.	To minimize dust impacts	MTR / Contractor	Concrete batching plant at works area V	Construction phase	To be implemented as per construction programme
Table 12.9 and Table 12.12	The design emission concentration of dust collector for different types of silos for concrete batching plant should be: ▪ Dust collector for each small Cement Silo ≤ 30 mg/m^3 ▪ Dust collector for each Large Capacity Cement Silo ≤ 50mg/m^3 ▪ Dust collector for each PFA Silo ≤ 30 mg/m^3 ▪ Dust collector for each Mixer ≤ 40 mg/m3 During operation of concrete batching plant:	To minimize dust impacts	MTR / Contractor	Concrete batching plant at works area V	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ The aggregates should be unloaded from the tipper trucks to the receiving hopper equipped with enclosures on 3 sides and top cover, and water spraying system. ▪ The cement and PFA should be directly loaded into the silo via a flexible duct. Dust collectors should be installed at the cement/PFA silo based on the above design emission rates. ▪ The aggregates should be stored in fully enclosed overhead storage bins. The top of overhead storage bins should be covered with cladding. Water spraying system should be installed at the top of storage bins for watering the aggregates, and aggregate storage bins should be fully enclosed. ▪ The whole process of weighing and mixing of cementitious material should be performed in a fully enclosed environment. The mixers shall equip with the dust collectors based on the above design emission rates. ▪ The concrete should be directly loaded from the mixer into the transit mixer of a truck in “wet” form.					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	▪ Haul road within the site should be paved. Wheel washing pit should be installed at the gate of the concrete batching plant. Water spraying system should be installed along the haul road.					
Table 12.10	(1) Cut & Cover Areas and Stockpiles in the vicinity of adits/shafts: (a) Heavy construction activities at Cut & Cover Areas, Storage of materials at Stockpiles - Active areas for heavy construction activities, loading & unloading materials at stockpiles ▪ The specified requirements for cut & cover areas and stockpiles at Shek Kong, Nam Cheong and West Kowloon works areas are as follows: (i) Shek Kong works area – active area minimized to 15% of total area, watering with complete coverage of active area ten times a day. (ii) Nam Cheong works area – active area minimized to 30% of total area, watering with complete coverage of active stockpile area four	To minimize dust impacts	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	times a day. (iii) West Kowloon works area – active area minimized to 15% of total area, watering with complete coverage of active area eight times a day. ▪ For other sites, the active area would be minimized to 30% of the total area, water spraying system would be applied on the active area and watering with complete coverage of active area four times a day would be required. ▪ The remaining inactive area would be well covered with impervious sheeting at all work sites. (b) Trucks - Transportation of materials ▪ Wheel wash facilities provided at the site exit. The vehicles should be washed before leaving the stockpiles. The spoils should also be well covered before leaving the site in order to minimise generation of dusty materials. ▪ The haul roads within the site should be paved and water spraying would be provided to keep the wet condition. ▪ For the Shek Kong works area, watering paved haul					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	roads once per hour would be provided. (2) Temporary stockpiles within barging facilities: (a) Loading point - Loading of spoils from trucks onto stockpile ▪ Water spraying should be provided at the loading points to suppress the dust impact. (b) Storage of materials - Active area for loading & unloading materials ▪ Water spraying system should be applied on the active area and watering with complete coverage of active area four times a day is required.					
Table 12.11	Barging facilities: (1) Haul road within barging facilities - Transportation of spoils to the barging points ▪ All road surfaces within the barging facilities should be paved and water spraying should be provided to keep the wet condition. For paved haul roads at West Kowloon and Nam Cheong, watering	To minimize dust impacts	MTR / Contractor	All barging points	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	haul road once per hour is required. (2) Unloading of materials - Unloading of spoil materials ▪ The unloading process should be undertaken within enclosed tipping hall. Water spraying and dust curtain should be provided at the discharge point for dust suppression. (3) Trucks - Vehicles leaving the barging facilities ▪ Vehicle wheel washing facilities should be provided at site exit. (4) Transportation of spoils to one of the Nam Cheong Barging Point ▪ Fully enclosed conveyor system should be adopted for transportation of spoils from shaft to the barging point.					
S 12.78	Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: ▪ Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces	To minimize dust impacts	MTR / Contractor	All works areas	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	and unpaved roads, particularly during dry weather. ▪ Use of frequent watering for particularly dusty construction areas and areas close to ASRs. ▪ Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines. ▪ Open stockpiles should be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. ▪ Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. ▪ Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. ▪ Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. ▪ Imposition of speed controls for vehicles on					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	unpaved site roads. 8 kilometers per hour is the recommended limit. ▪ Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs. ▪ Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. ▪ Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed. ▪ Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.					
S12.94	Environmental monitoring and audit for dust emission should be conducted in accordance with EM&A Manual during the construction phase of the Project to check	To monitor dust impact	MTR / Contactor	Proposed monitoring locations	Design and operation phases	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	compliance with legislative requirements.					
Air Quality (Operation Phase)						
S12.48	The vent shafts of the stations should be designed to be sited at more than 5m from any opening at the adjacent building	To alleviate the adverse air quality impact in the stations	MTR	WKT	Design and operation phases	To be implemented as per construction programme
S12.50	The design of the mechanical air ventilation for PTI should follow EPD's ProPECC PN1/98 Control of Air Pollution in Semi-confined Public Transport Interchanges.	To alleviate the adverse air quality impact in the PTI	MTR	PTI at the ground floor of ventilation building complex at WKT	Design and operation phases	To be implemented as per construction programme
Hazard to Life						
S13.96/ S13.99	Improved truck design to reduce the amount of combustibles in the cabin and fuel carried in the fuel tank should be minimised to reduce the duration of any fire.	To meet the ALARP requirement	MTRC/ Contractor	-	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	The truck should be brand new, diesel powered and equipped with fuel and battery isolation switches, front exhaust spark arrester, 1 x 9 kg water based and 1 x 9 kg dry chemical powder fire extinguishers. This should be combined with monthly vehicle inspection					
S13.96	The explosive truck accident frequency should be minimized by implementing a dedicated training programme for both the driver and his attendants, including regular briefing sessions, implementation of a defensive driving attitude. In addition, drivers should be selected based on good safety record, and medical checks.	To meet the ALARP requirement	MTRC/ Contractor	-	Construction phase.	Implemented
S13.96	The contractor should as far as practicable combine the explosive deliveries for a given work area.	To meet the ALARP requirement	MTRC/ Contractor	-	Construction phase	Implemented
S13.96	The explosive truck fire involvement frequency should be minimized by implementing a better emergency response and training to make sure the adequate fire extinguishers are used and attempt is made to evacuate the area of the	To meet the ALARP requirement	MTRC/ Contractor	-	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	incident or securing the explosive load if possible. All explosive vehicles should also be equipped with bigger capacity AFFF-type extinguishers.					
S13.96	A minimum headway between two consecutive truck conveys of at least 10 min is recommended	To meet the ALARP requirement	MTRC/ Contractor	Along explosives transport route.	Construction phase.	Implemented
S13.96/ S13.105	Only the required quantity of explosives for a particular blast should be transported to avoid the return of unused explosives to the magazines. If disposal is required for small quantities, disposal should be made in a controlled and safe manner by a Registered Shotfirer.	To reduce the risk during explosives transport	MTRC/ Contractor	-	Construction phase	Implemented
S13.97	Blasting activities including storage and transport of explosives should be supervised and audited by competent site staff to ensure strict compliance with the blasting permit conditions.	To ensure that the risks from the proposed explosives storage and transport would be	MTRC / Contractor	Works areas at which explosives would be	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
		acceptable		stored and/or used.		
S13.97	Emergency plan (ie magazine operational manual) shall be developed to address uncontrolled fire in magazine area and transport. The case of fire near an explosive carrying truck in jammed traffic should also be covered. Drill of the emergency plan should be carried out at regular intervals.	To reduce the risk of fire	MTRC/ Contractor	Explosive Magazine and along explosives transport route.	Construction phase	Implemented
S13.97	Adverse weather working guideline should be developed to clearly define procedure for transport explosives during thunderstorm.	To ensure safe transport of explosives	MTRC/ Contractor	Along explosives transport route.	Construction phase	Implemented
S13.98	Delivery vehicles shall not be permitted to remain within the secured fenced off magazine store area.	To reduce the risk of fire within the magazine	MTRC / Contractor	Explosive Magazine	Construction phase	Implemented
S13.98	Good house-keeping within and outside of the magazine to ensure that combustible materials (including vegetation) are removed and not allowed to accumulate.	To reduce the risk of fire within the magazine	MTRC / Contractor	Explosive Magazine	Construction phase	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S13.99/ S13.101	Use only experienced driver(s) with good safety record. Training should be provided to ensure it covers all major safety subjects.	To ensure safe transport of explosives	MTRC/ Contractor	-	Construction phase	Implemented
S13.99	Develop procedure to ensure that parking space on the site is available for the explosive truck. Confirmation of parking space should be communicated to truck drivers before delivery.	To ensure that the risks from the proposed explosives storage and transport would be acceptable	MTRC/ Contractor	Explosive magazine	Construction phase	Implemented
S13.99	Detonators shall not be transported in the same vehicle with other Class 1 explosives	To reduce the risk of explosion during the transport of cartridge emulsion	MTRC / Contractor	-	Construction phase	Implemented
S13.99	During transport of the explosives within the tunnel, hot work should not be permitted in the vicinity of the explosives offloading or charging activities.	To ensure safe transport of explosives	MTRC/ Contractor	Along explosives transport route.	Construction phase	Implemented
S13.99	Ensure that packaging of detonators remains intact until	To reduce the risk of	MTRC/	-	Construction	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	handed over at blasting site.	explosion during the transport of detonator	Contractor		phase	
S13.99	Horizontal fire screen on cargo deck and vertical fire screen mounted at least 150 mm behind the drivers cab and 100 mm from the steel cargo compartment, the vertical screen shall protrude 150 mm in excess of all three (3) sides of the steel cargo compartment.	To reduce the risk during explosives transport	MTRC/ Contractor	-	Construction phase	Implemented
S13.104	Ensure that cartridge emulsion with high water content should be preferred. Also, the emulsion with perchlorate formulation should be avoided.	To ensure safe explosives to be used	MTRC/ Contractor	-	Construction phase	Implemented
Landfill Gas Hazard – Design and Construction Phases						
S14.73 & S14.86	- All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of excavations. Safety notices should be posted warning of the potential hazards.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone, Barging Point	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
				and Nursery Site		
S14.73	- Those staff who work in, or have responsibility for "at risk" areas, including all excavation workers, supervisors and engineers working within the Consultation Zone, should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
S14.73	- During all works, safety procedures will be implemented to minimise the risks of fires and explosions and asphyxiation of workers (especially in confined space).	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
S14.73	- Safety officers, specifically trained with regard to landfill gas related hazards and the appropriate actions to take in adverse circumstances will be present on all worksites throughout the works.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation	Construction phase	To be implemented as per construction

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
				Zone		programme
S14.73, S14.86, S14.87	- Smoking and naked flames will be prohibited within confined spaces. 'No Smoking' and 'No Naked Flame' notices in Chinese and English will be posted prominently around the construction site. Safety notices should be posted warning of the potential hazards.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone, Barging Point and Nursery Site	Construction phase	To be implemented as per construction programme
S14.73	- Welding, flame-cutting or other hot works may only be carried out in confined spaces when controlled by a 'permit to work' procedure, properly authorised by the Safety Officer. The permit to work procedure will set down clearly the requirements for continuous monitoring of methane, carbon dioxide and oxygen throughout the period during which the hot works are in progress. The procedure will also require the presence of an appropriately qualified person who	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	shall be responsible for reviewing the gas measurements as they are made, and who shall have executive responsibility for suspending the work in the event of unacceptable or hazardous conditions. Only those workers who are appropriately trained and fully aware of the potentially hazardous conditions which may arise will be permitted to carry out hot works in confined areas.					
S14.73	- A mechanical ventilation system must be in use at all times during which personnel are engaged in works inside the tunnel or excavation and be evacuated in the event of power outages. Work must not be carried out in the absence of mechanical ventilation and supervision of adequately trained safety personnel. In exceptional case where work is carried out under non-ventilated condition, any electrical equipment used, such as motors and extension cords, should be intrinsically safe.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S14.73	- Adequate fire extinguishing equipment, fire-resistant clothing and breathing apparatus sets should be made available on site.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
S14.86	- Raising the site office 500mm above ground.	Protect the workers from landfill gas hazards	Contractor	Barging Point	Construction phase	To be implemented as per construction programme
S14.86	- Utilities services connected to the site office and the annulus around these service entry points should be properly sealed.	Protect the workers from landfill gas hazards	Contractor	Barging Point	Construction phase	To be implemented as per construction programme
S14.74	- Construction works to be undertaken in confined space should follow the relevant Regulations under Chapter 59 Factories and Industrial Undertakings	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML	Construction phase	To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	Ordinance and Chapter 509 Occupational Health and Safety Ordinance.			Consultation Zone		construction programme
S14.73	- Monitoring of methane, carbon dioxide and oxygen inside the XRL tunnels.	Protect the workers from landfill gas hazards	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
S14.75	- A walkover survey to monitor flammable gas at all joints and cracks, if identified, upon completion of the tunnel work. Rectifications, such as sealing of cracks and inspection of tunnel seals, shall be carried out for any signs of the presence of flammable gas. The survey should be conducted under non-ventilated condition and before starting the work of the day.	Confirm no landfill gas ingress into the XRL tunnels	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
S14.76	- Weekly monitoring of methane, carbon dioxide and oxygen in the form of a walkover survey at 20m intervals for section of tunnels under NTML and 50m	Confirm no landfill gas ingress into the XRL tunnels	Contractor	XRL tunnels within the NTML	Construction phase	To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	interval within the NTML Consultation Zone should be conducted after completion of the tunnel construction works and not less than 3 months before commencement of operation. The survey should be conducted under non-ventilated condition and before starting the work of the day.			Consultation Zone		construction programme
S14.77	- A summary of the monitoring results should be submitted to EPD for record before the commencement of operational phase. The results should be reviewed and agreed with EPD before the commencement of operation to determine the monitoring requirements during the operational phase	To review and agree the monitoring requirement during the operational phase	MTR/ Contractor	-	Before operation	To be implemented as per construction programme
S14.78	- Appropriate sealant will be applied to joints to prevent the ingress of groundwater, which will also form a low permeability gas barrier. Good workmanship and adequate construction supervision will be required to ensure the actual works are implemented as per the design requirements. This	Protect the XRL tunnels from landfill gas hazards	Design Engineer/ Contractor	XRL tunnels within the NTML Consultation Zone	Design and Construction phases	To be implemented as per construction programme

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	will be implemented by MTRC's Material and Workmanship Specification.					
S14.79	- Adequate ventilation will be needed as part of the tunnel design to act as an active gas control when needed.	Protect the XRL tunnels from landfill gas hazards	Design Engineer	XRL tunnels within the NTML Consultation Zone	Design phase	To be implemented as per construction programme
S14.80	- Upon completion of the landfill gas protection measures, a report on the implemented landfill gas protection measures with relevant as-built drawings and other detailed information showing that the design measures mentioned in this assessment to protect the tunnels from landfill gas hazard have been properly incorporated should be submitted to EPD.	Ensure landfill gas protection measures have been completed	Contractor	XRL tunnels within the NTML Consultation Zone	Construction phase	To be implemented as per construction programme
Landfill Gas Hazard – Operation Phase						
S14.76	- Ventilation of the tunnels should be switched on for half an hour before the first train is expected (the	Protect the operation of the XRL from landfill gas	MTR	XRL tunnels within the	Operation phase	To be implemented


EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	requirement to implement this measure is subject to findings of the review of landfill gas monitoring data with EPD before the commencement of operation).	hazards		NTML Consultation Zone		as per construction programme
S14.76	- All maintenance personnel and station staff working within the tunnels should be educated in the dangers of landfill gas and the signs and symptoms of asphyxia.	Protect the workers from landfill gas hazards	MTR	XRL tunnels within the NTML Consultation Zone	Operation phase	To be implemented as per construction programme
S14.76	- Smoking within the tunnels should be prohibited at all times.	Protect the operation of the XRL and workers from landfill gas hazards	MTR	XRL tunnels within the NTML Consultation Zone	Operation phase	To be implemented as per construction programme
S14.76	- An assumed presence of landfill gas should be adopted at all times by maintenance workers and a strictly regulated “work permit procedure” involving training, ventilation, gas monitoring (as detailed in	Protect the workers from landfill gas hazards	MTR	XRL tunnels within the NTML Consultation	Operation phase	To be implemented as per construction


EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	the Construction recommendations section), safety tracking and communication with maintenance staff, enforcement of the no smoking order.			Zone		programme
S14.82 & S14.83	- The monitoring requirement during the operational phase should be discussed with EPD before the commencement of operation. Weekly monitoring of methane, carbon dioxide and oxygen in the form of a walkover survey at 20m intervals for section of tunnels under NTML and 50m interval within the NTML Consultation Zone is tentatively proposed. The survey should be conducted under non-ventilated condition and before the first train operates and start-up of ventilation, if applicable. A summary of the monitoring results should be submitted to EPD for record at the end of the monitoring period.	Confirm no landfill gas ingress into the XRL tunnels	MTR	XRL tunnels within the NTML Consultation Zone	Operation phase	To be implemented as per construction programme
S14.84	- An annual walkover survey in the tunnels within the Consultation Zone of the NTML should be conducted to test for the presence of flammable gas at joints and	Confirm no landfill gas ingress into the XRL	MTR	XRL tunnels within the NTML	Operation phase	To be implemented as per

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
	cracks, if identified. Rectifications, such as sealing of cracks and inspection of tunnel seals, should be carried out for any signs of presence of flammable gas. The survey should be conducted under non-ventilated condition and before the first train operates and start-up of ventilation, if applicable.	tunnels		Consultation Zone		construction programme


Appendix D

Monitoring Locations

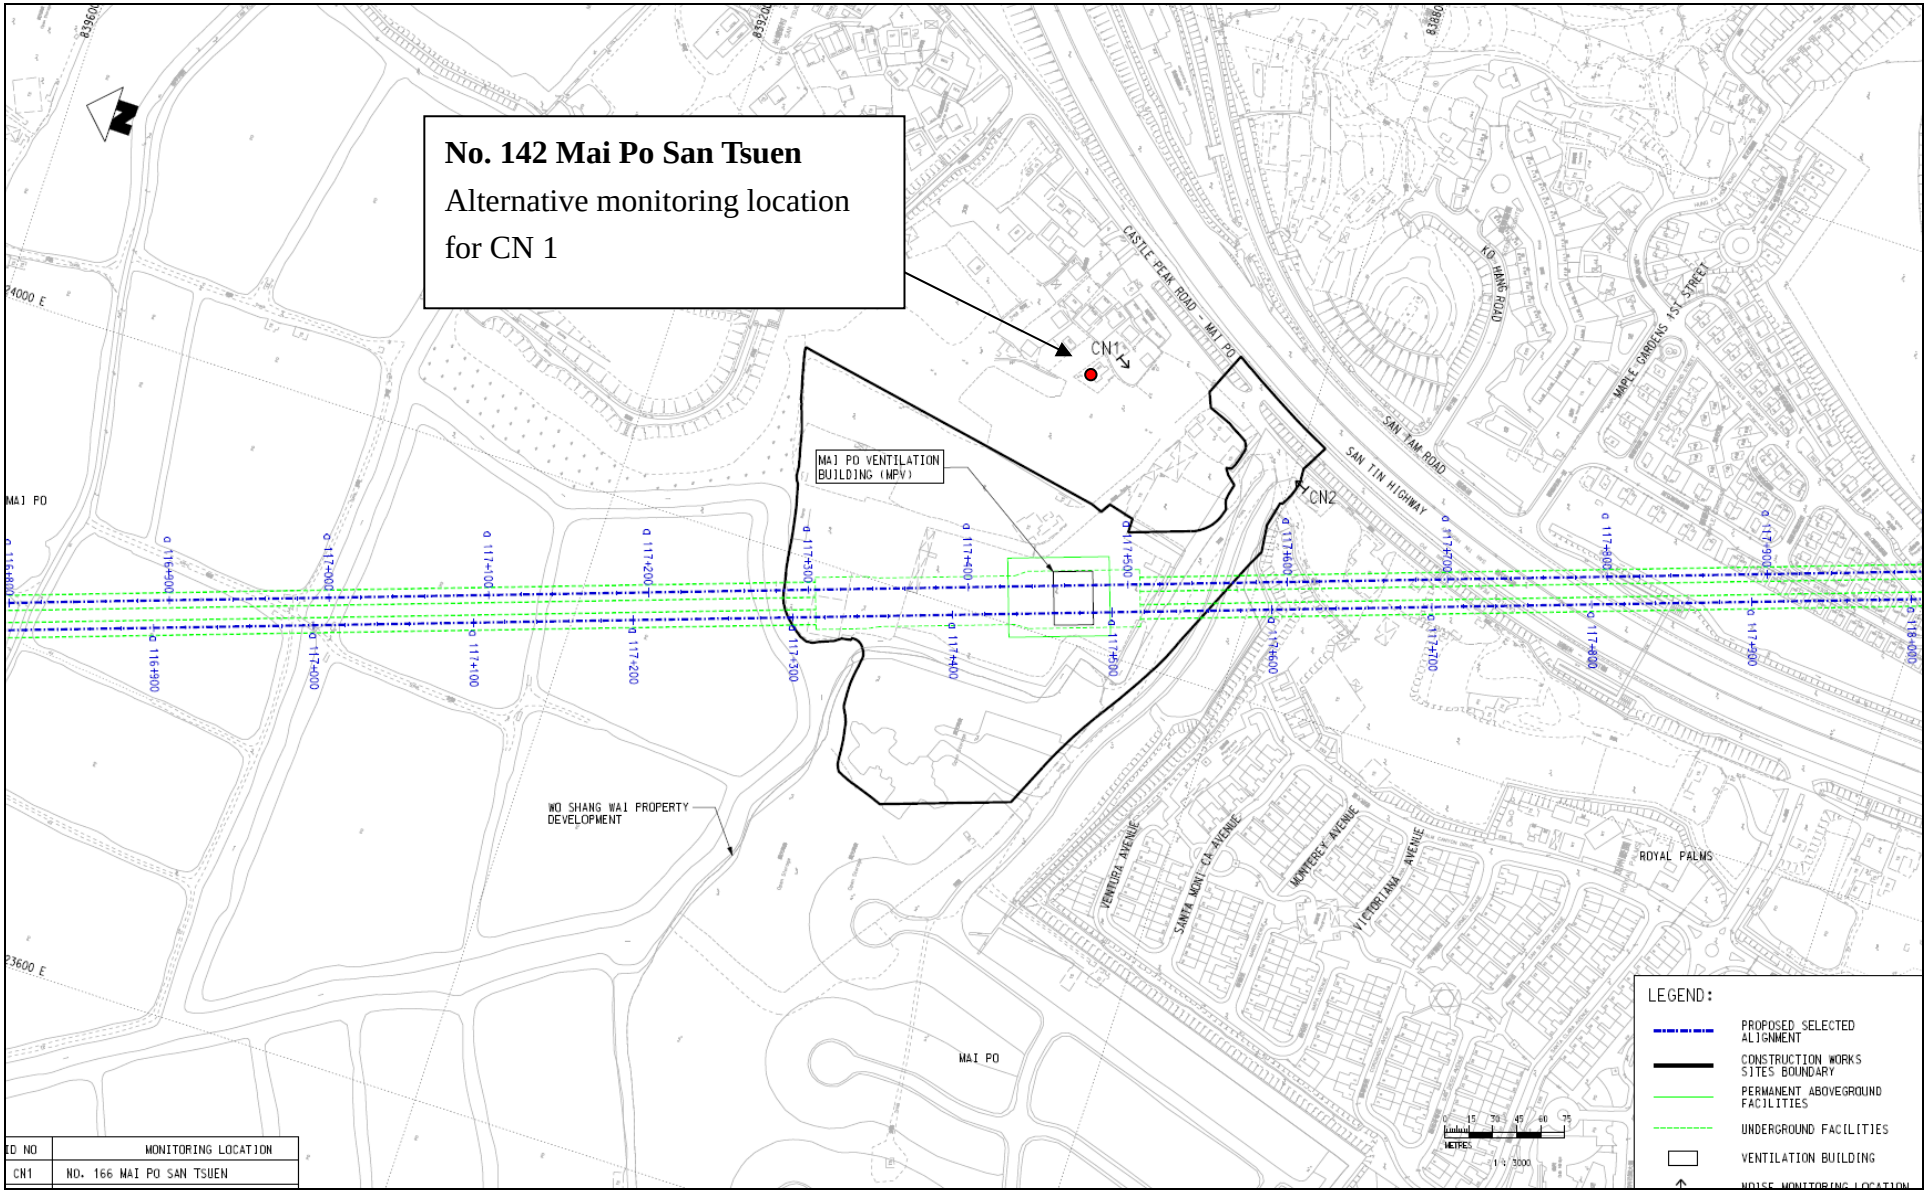
No. 142 Mai Po San Tsuen
Alternative monitoring location for CN 1
CN1
CN2
MAI PO VENTILATION BUILDING (MPV)
WO SHANG WAI PROPERTY DEVELOPMENT
MAI PO
CASTLE PEAK ROAD - MAI PO
KO HANG ROAD
MAPLE GARDENS
1ST STREET
SAN TAM ROAD
SAN TIN HIGHWAY
VENTURA AVENUE
SANTA MONICA AVENUE
MONTEREY AVENUE
VICTORIANA AVENUE
ROYAL PALMS
24000 E
23600 E
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
NOISE MONITORING LOCATION
METRES
1 : 3000
ID NO
MONITORING LOCATION
CN1
NO. 166 MAI PO SAN TSUEN

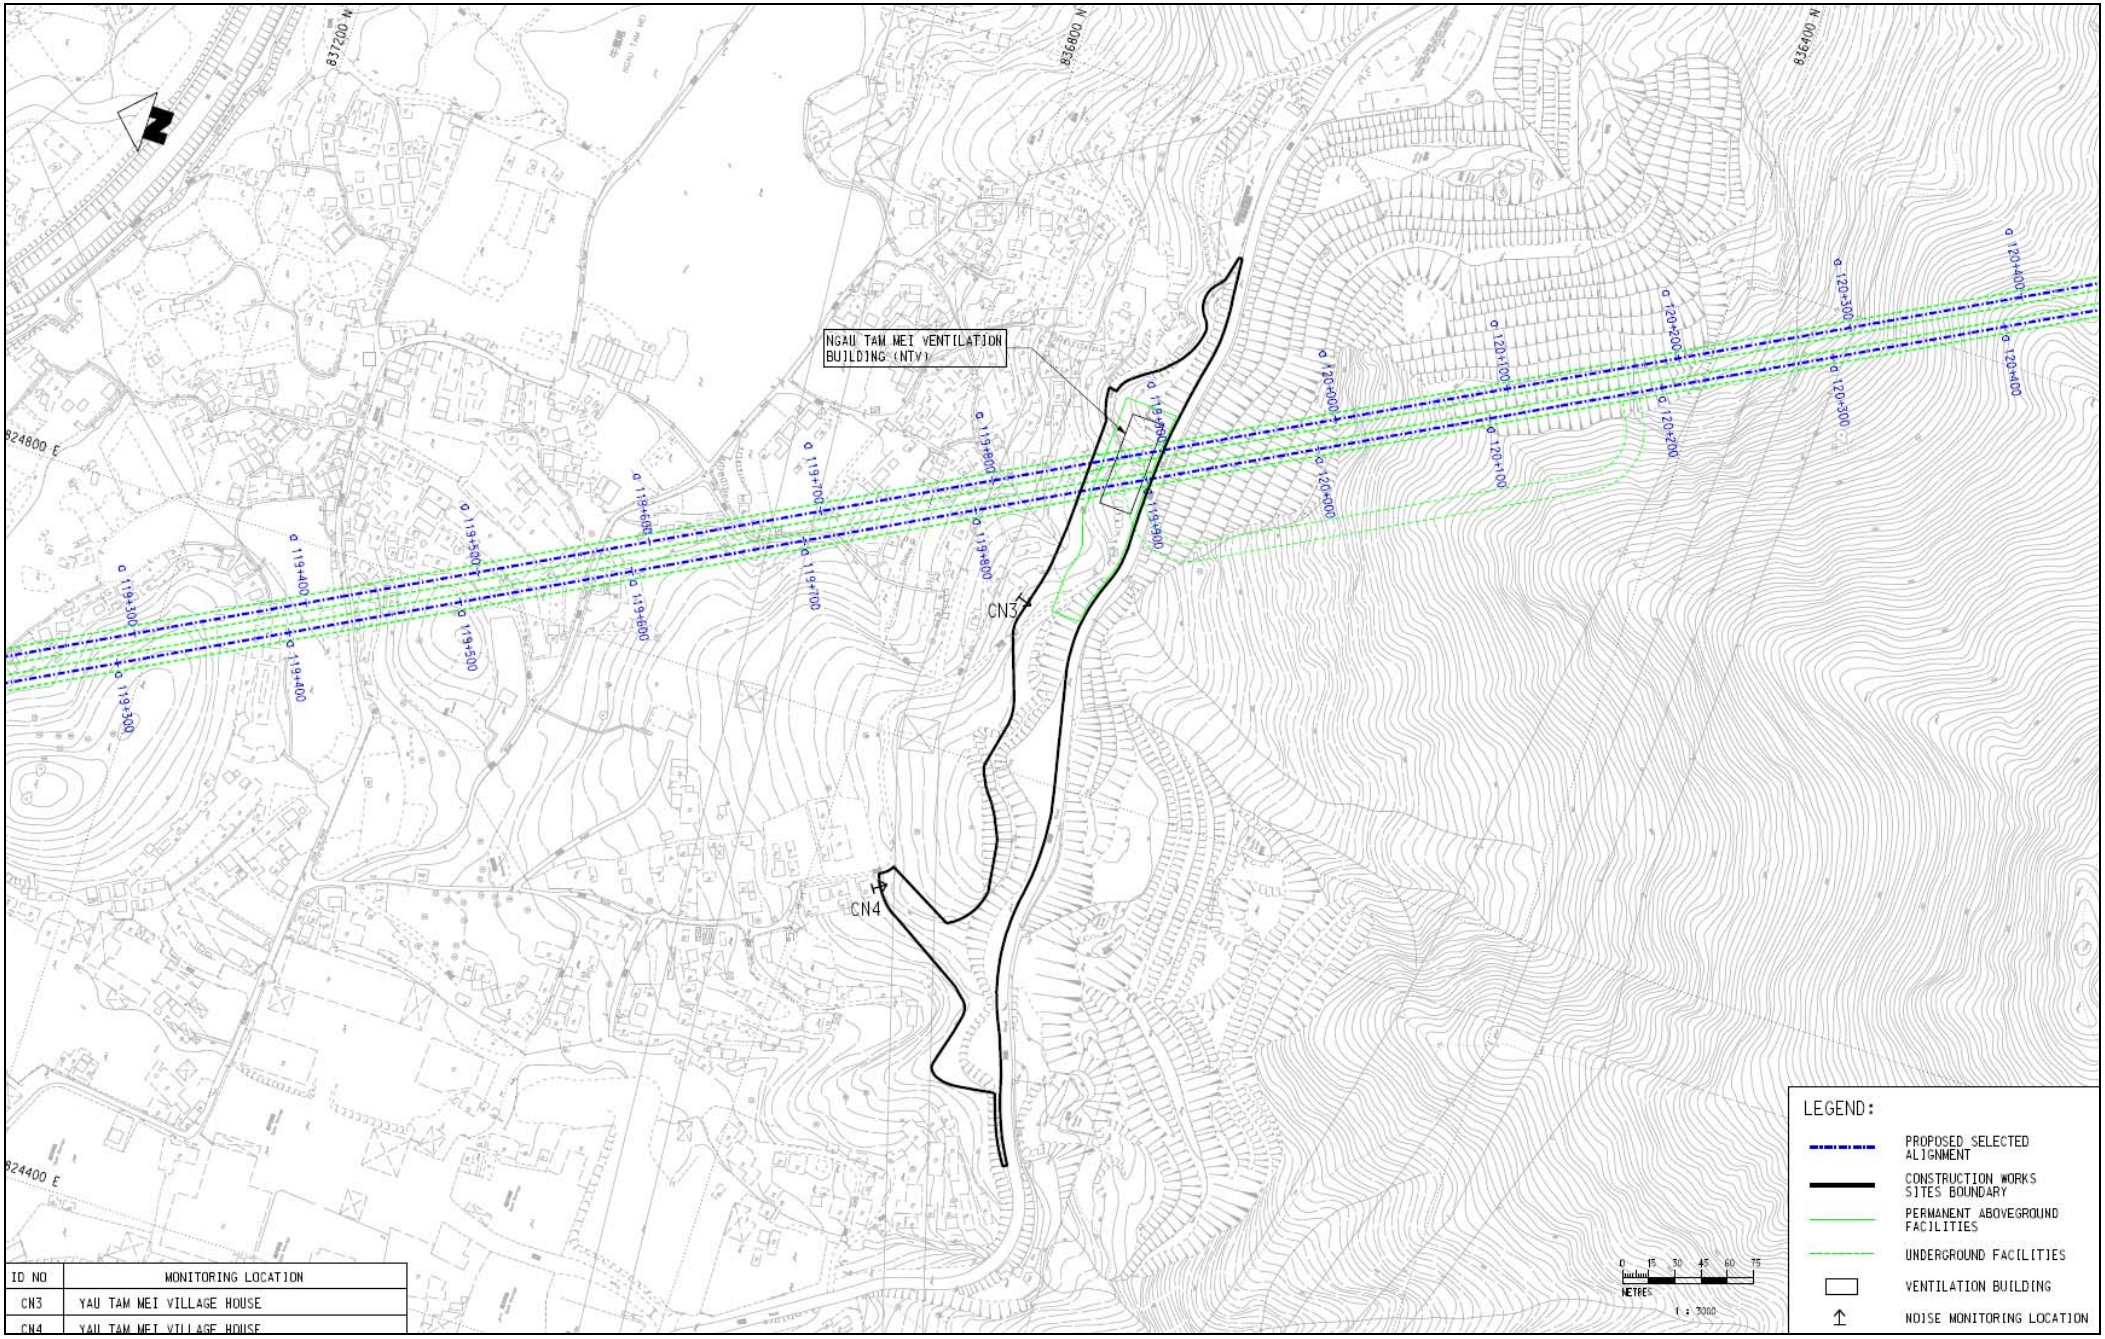

ID NO	MONITORING LOCATION
CN3	YAU TAM MEI VILLAGE HOUSE
CN4	YAU TAM MEI VILLAGE HOUSE

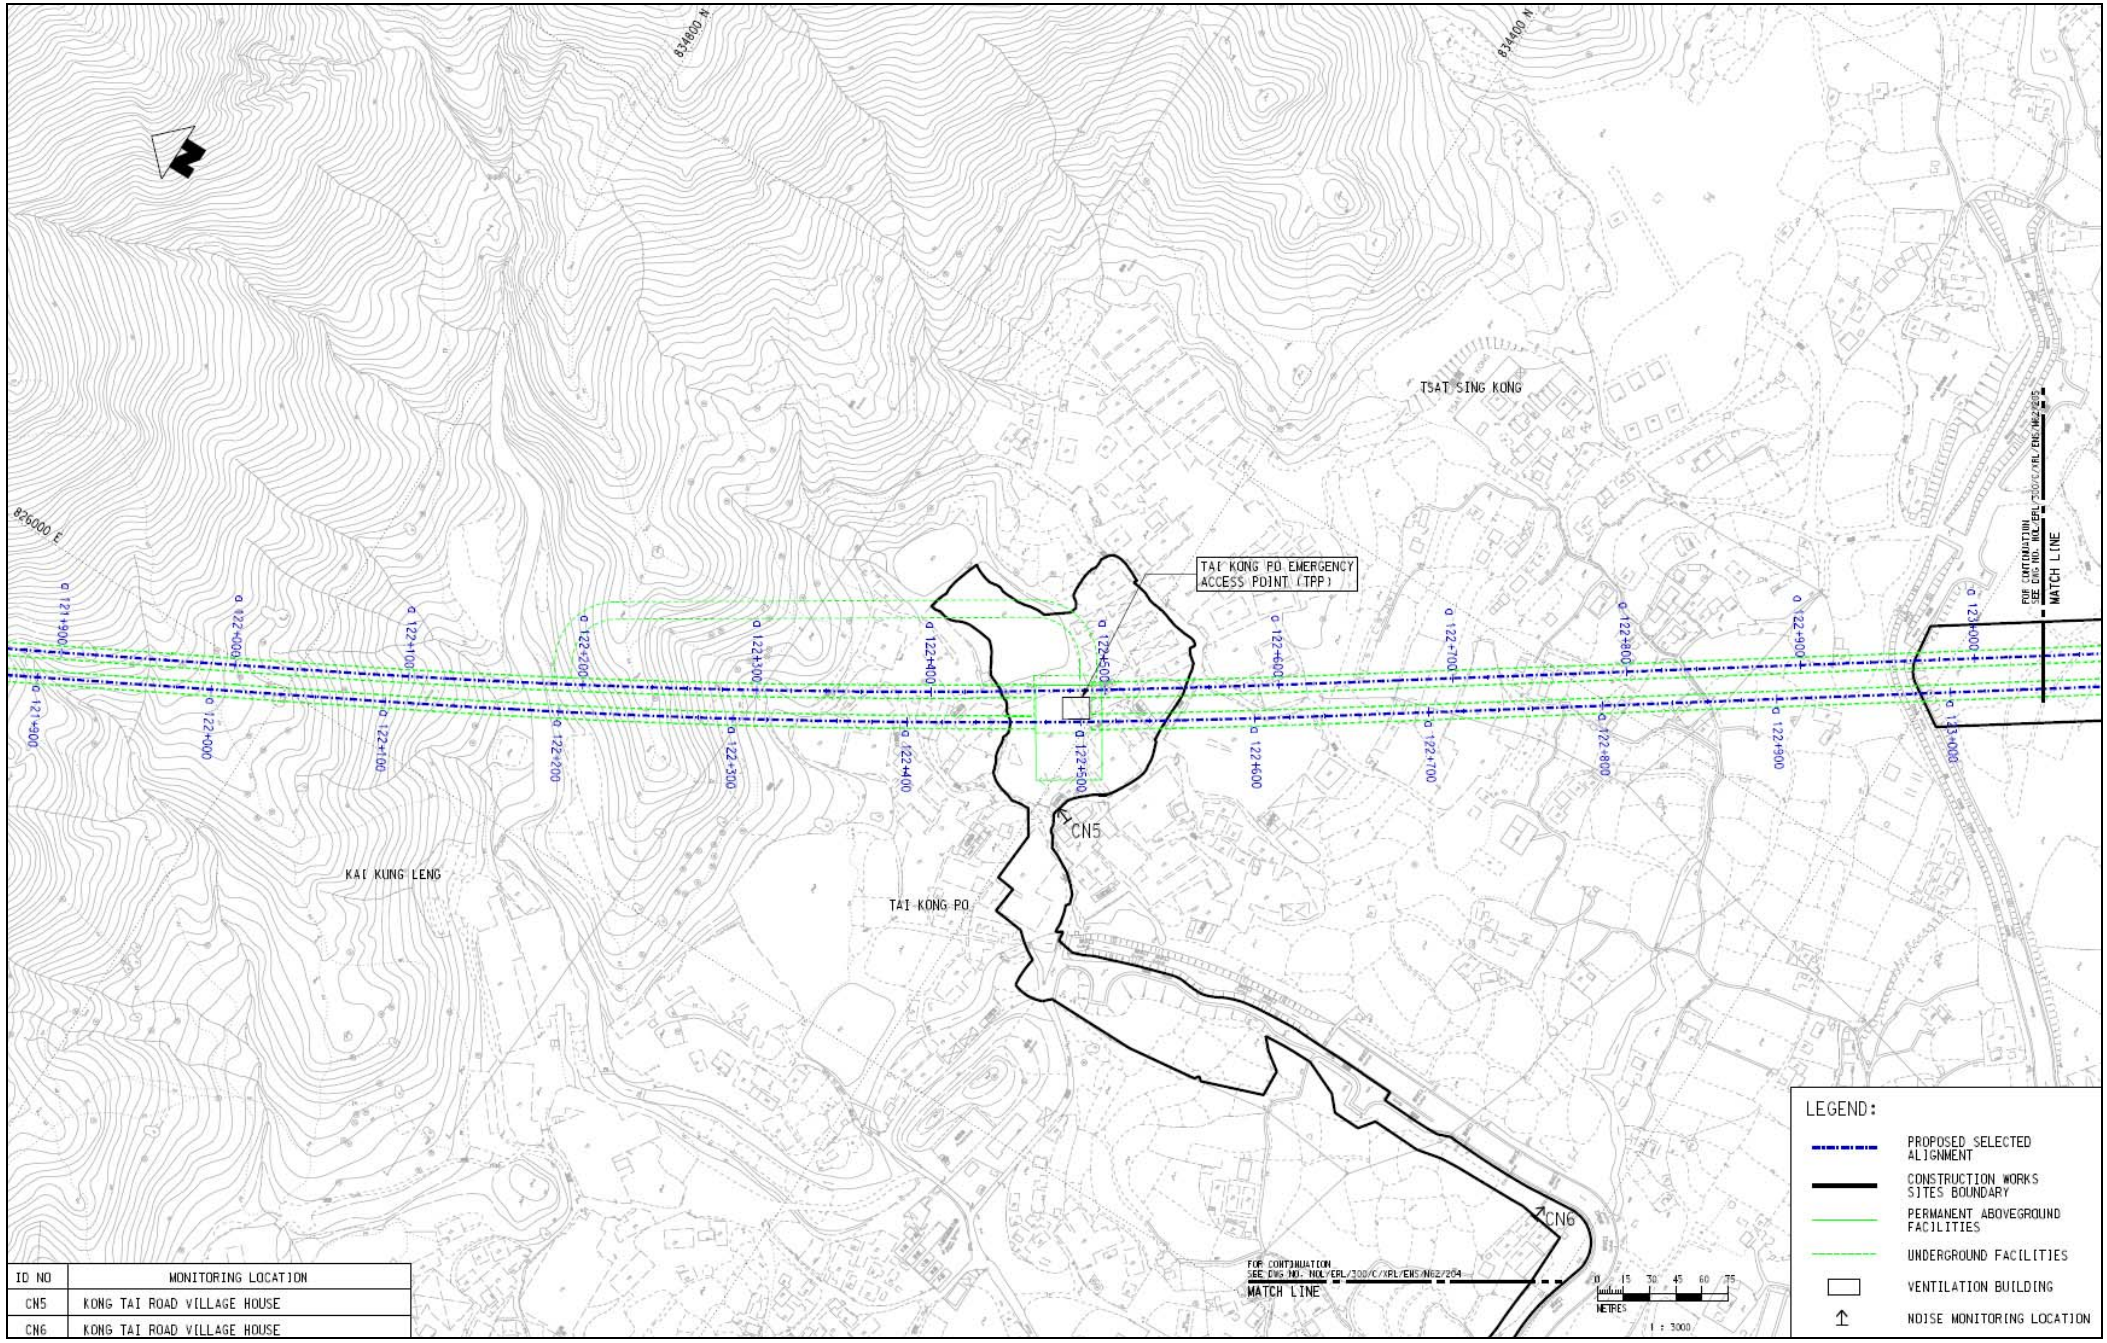

ID NO	MONITORING LOCATION
CN5	KONG TAI ROAD VILLAGE HOUSE
CN6	KONG TAI ROAD VILLAGE HOUSE




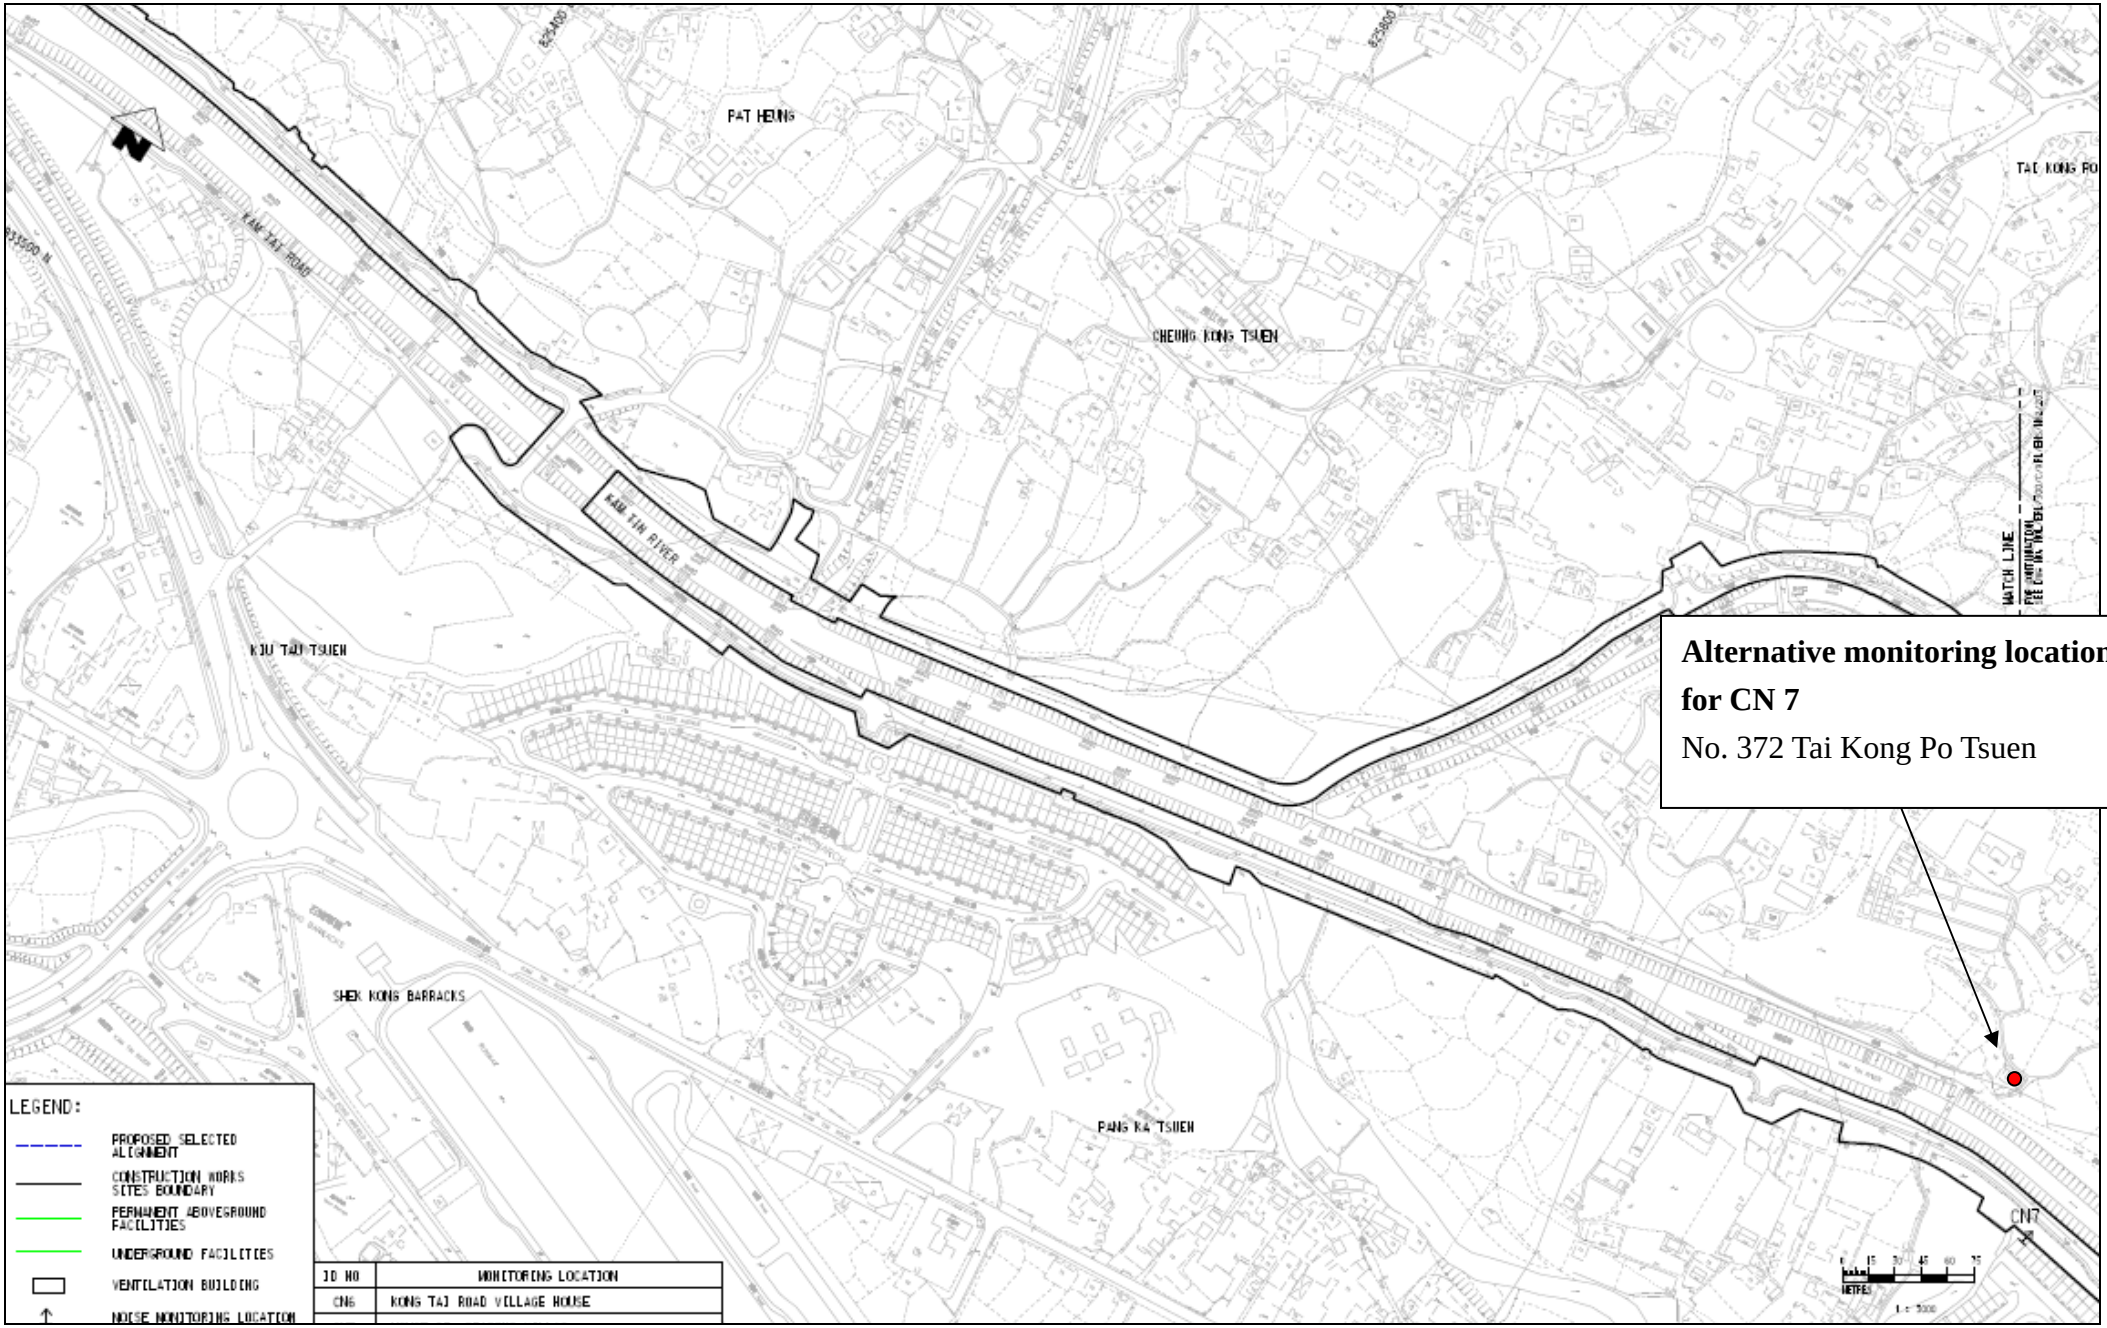


Figure 2 – Noise Monitoring Locations



Alternative monitoring location for CN 9
Leung Uk Tsuen Village House
EMERGENCY RESCUE STATION
LEUNG UK TSUEN
CN9
CN8
CN10
CN7
E.R HOLDING AREA
ACCESS ROAD
MAINTENANCE SHED
S.K.S. MAIN BLDG
GATE HOUSE
TRACTION P.(CLP)
CAR PARK
KENNEL
SHEK KONG STABLING SIDINGS
LAY DOWN AREA
CIVIL/BUILDING E&M
OHL BUILDING
PLANT ROOM
SIGNALING B.
PERMANENT W.
LAY DOWN AREA
RW01
RW02
RW03
D.G.S.
COCO BLDG
DIESEL S.
KAM TAI ROAD
KAM TIN RIVER
KAM TIN ROAD
CHURCH
PETROL STATION
WORK SHOP
SHEK KONG BARRACKS (PLA)
SPORTS GROUND
MATCH LINE
826800 E
826400 E
833600 N
833200 N
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
NOISE MONITORING LOCATION
METRES
1 : 3000
ID NO | MONITORING LOCATION
CN7 | HOUSE93, SEASONS VILLAS
CN8 | DD110 LOT 482, WANG TOI SHAN
CN9 | LEUNG UK TSUEN VILLAGE HOUSE
CN10 | LEUNG UK TSUEN SQUATS

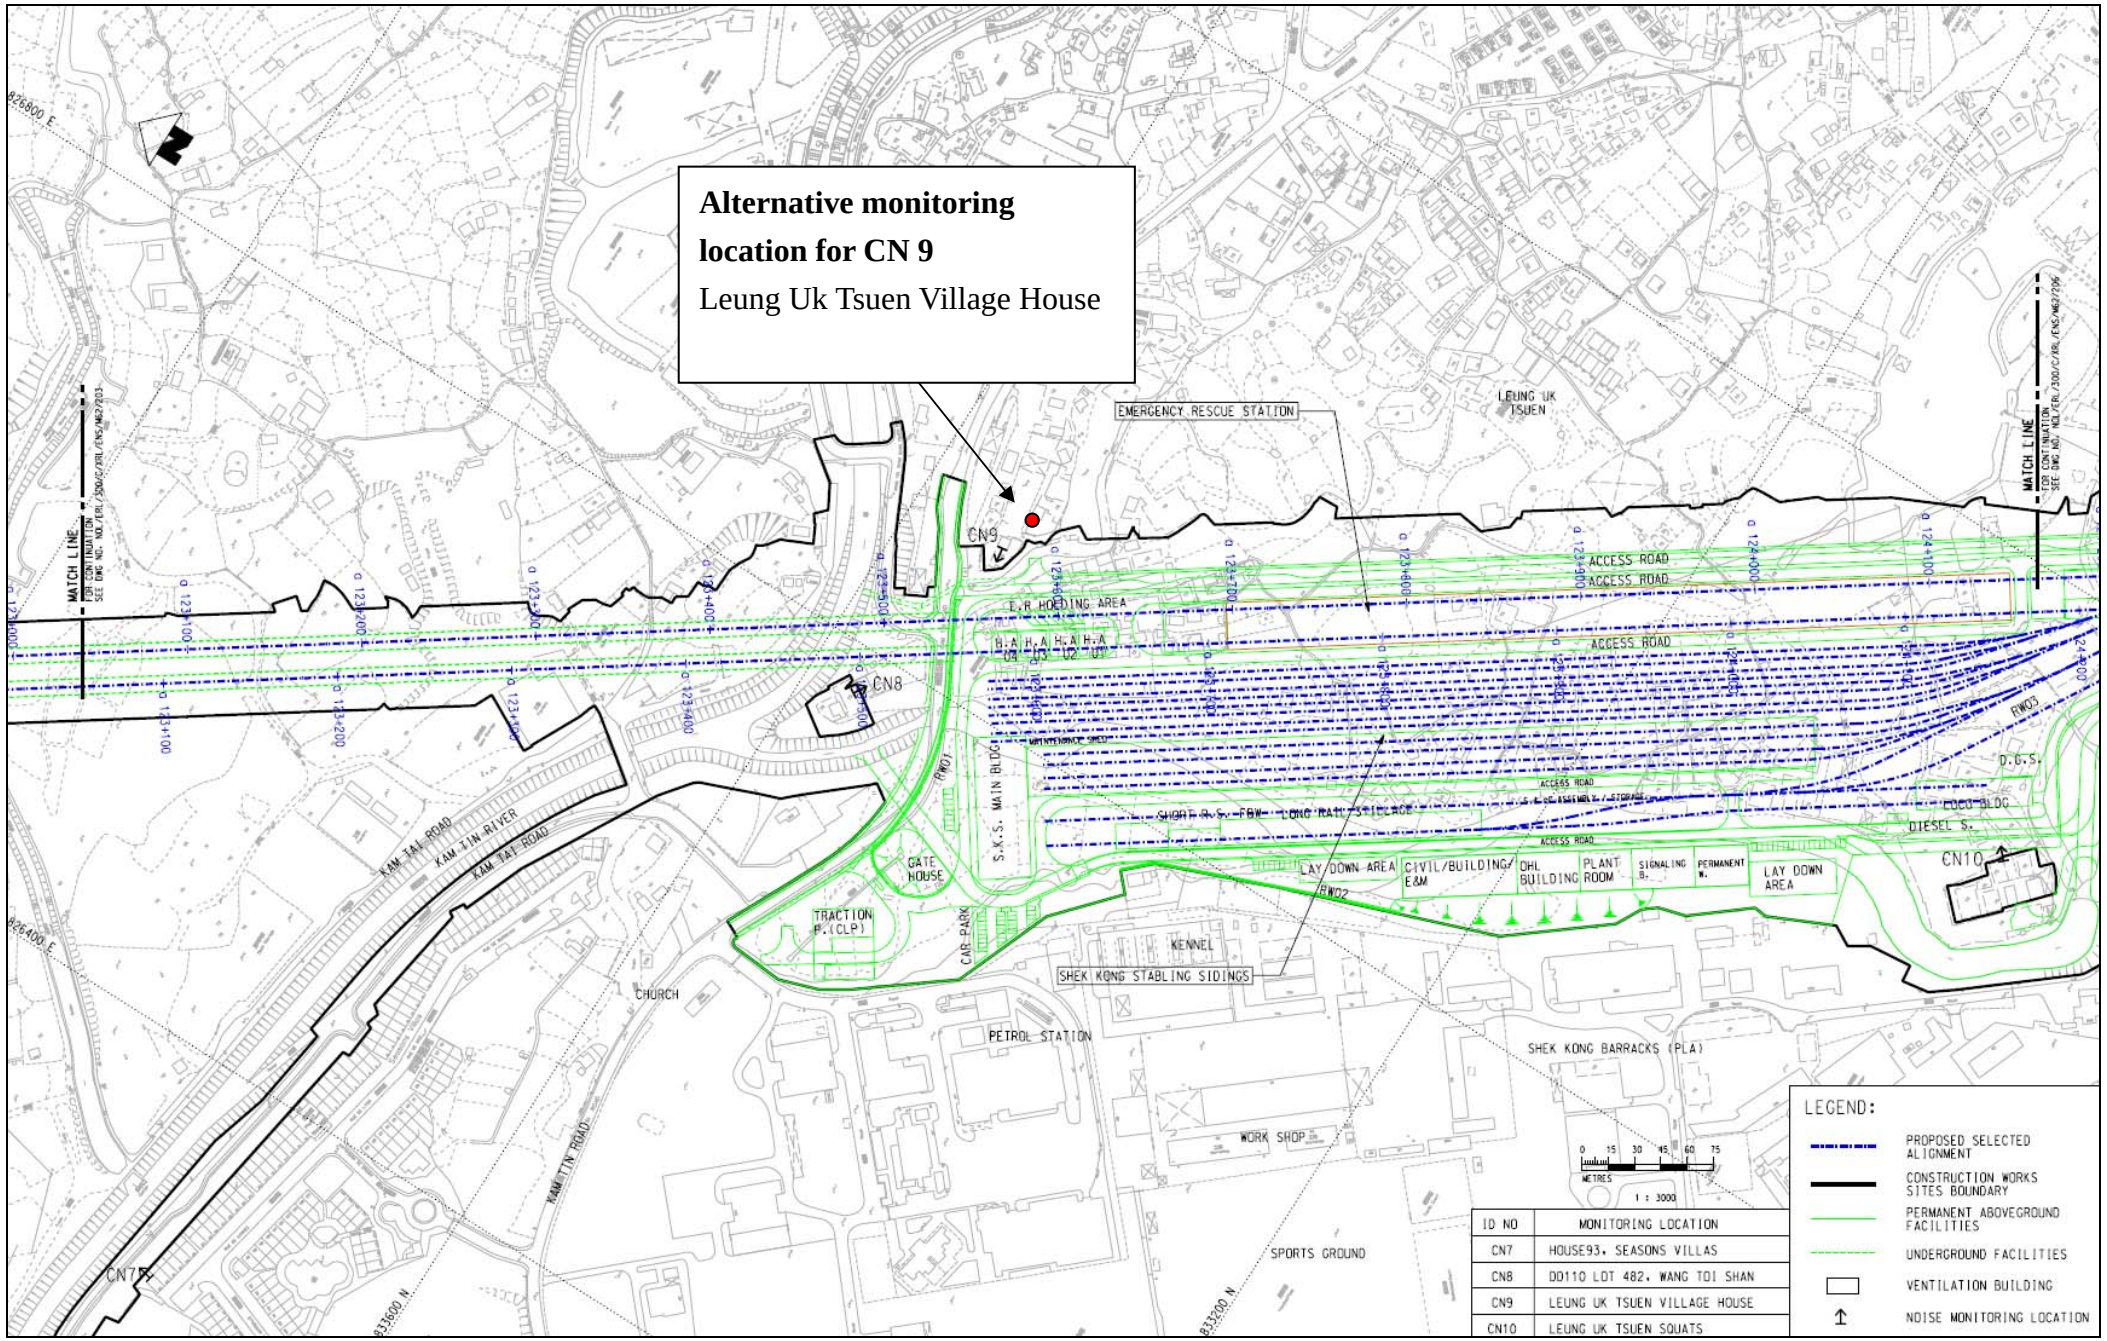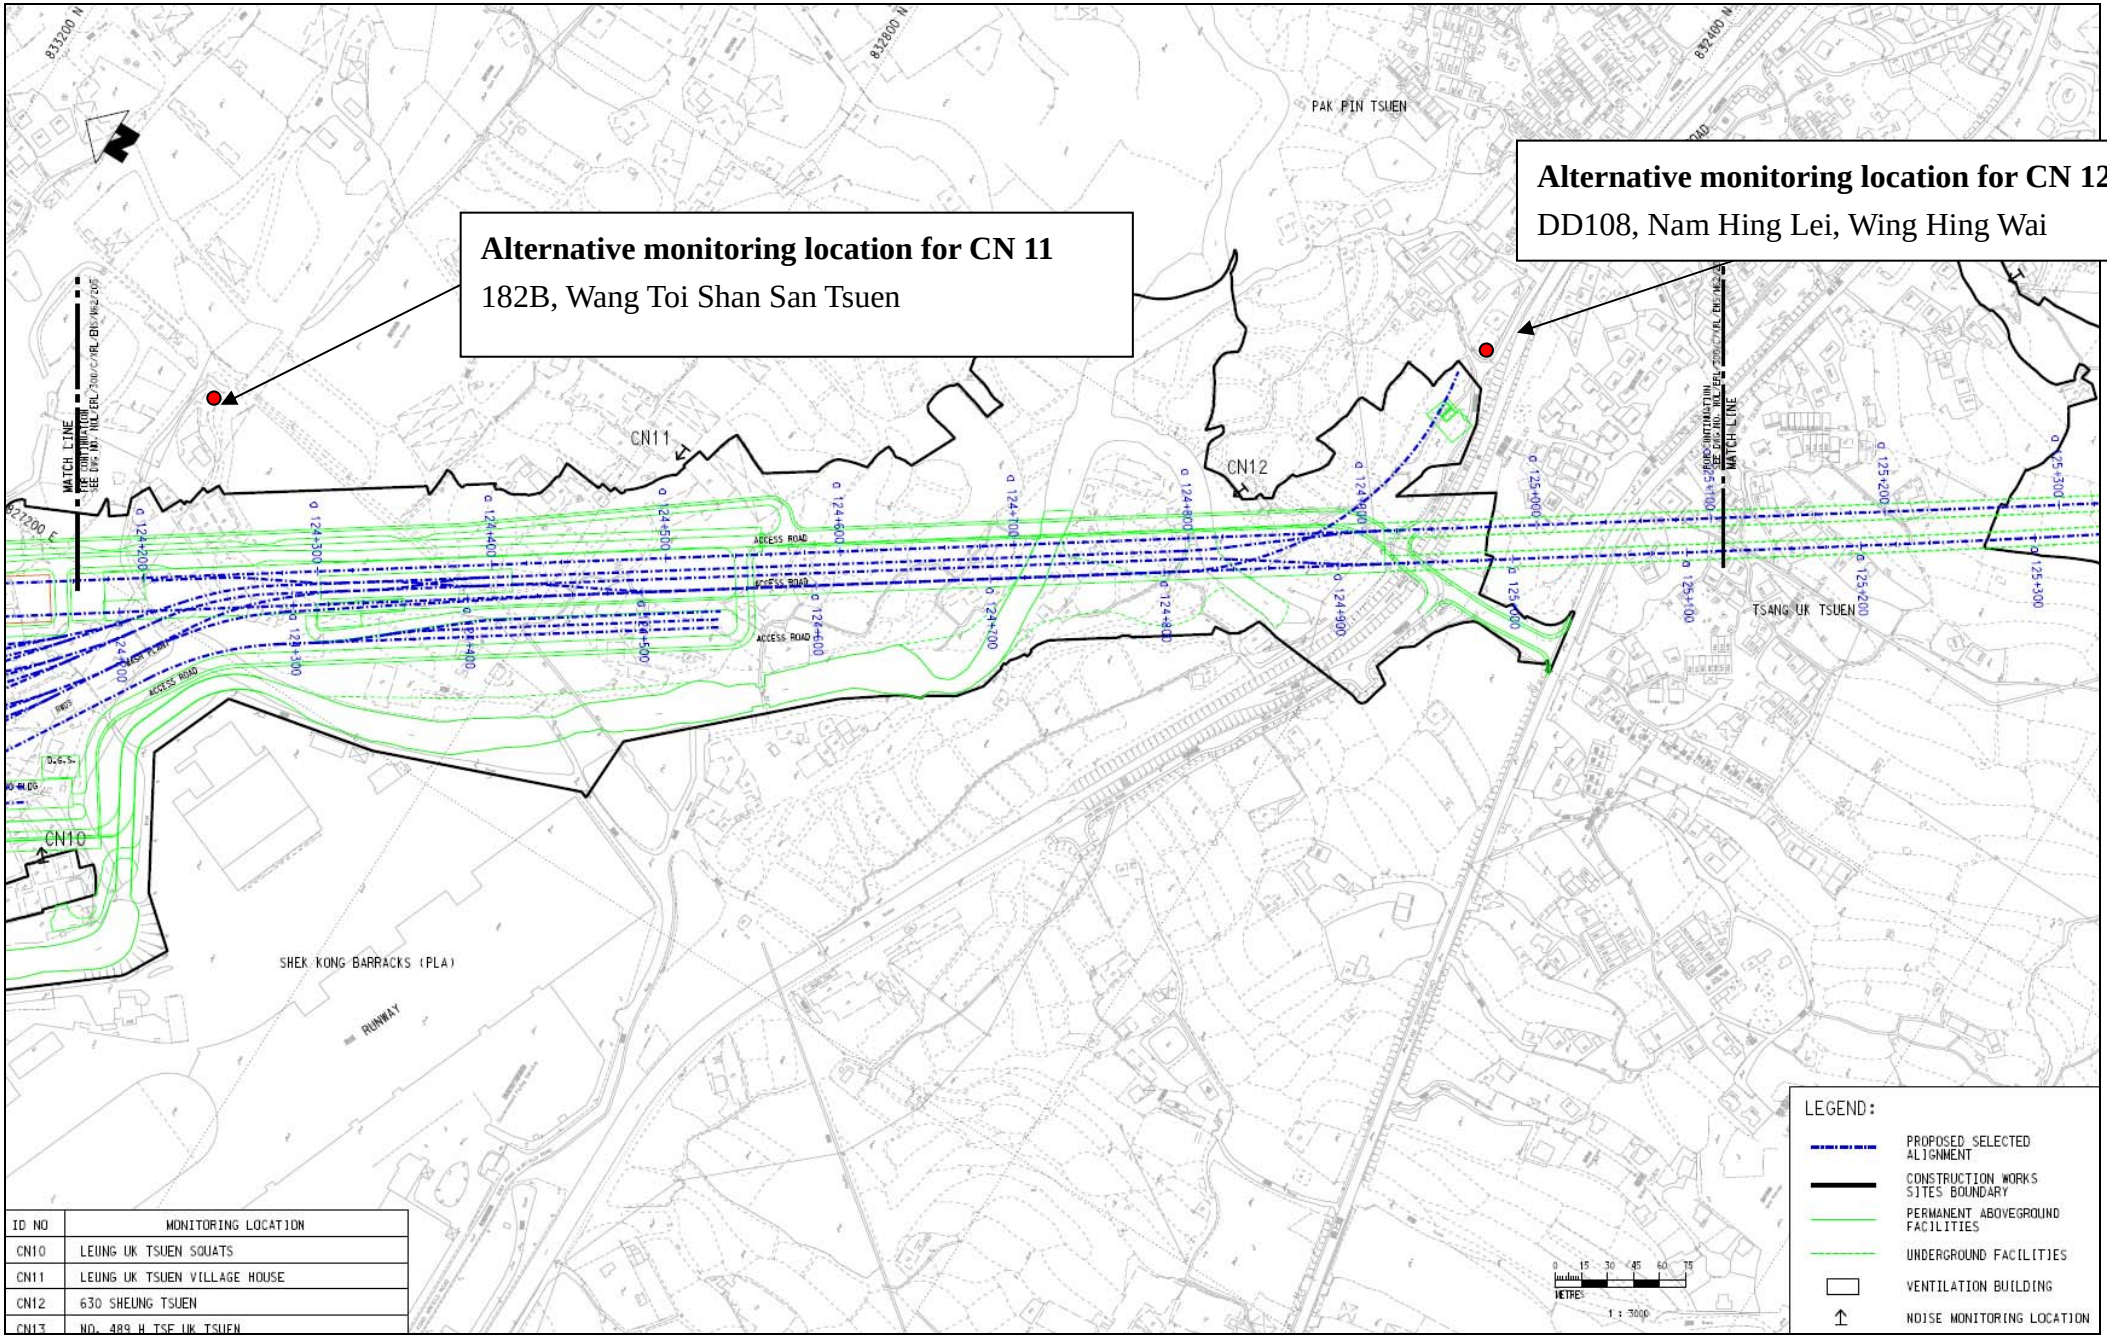

ID NO	MONITORING LOCATION
CN10	LEUNG UK TSUEN SQUATS
CN11	LEUNG UK TSUEN VILLAGE HOUSE
CN12	630 SHEUNG TSUEN
CN13	NO. 489 H TSE UK TSUEN

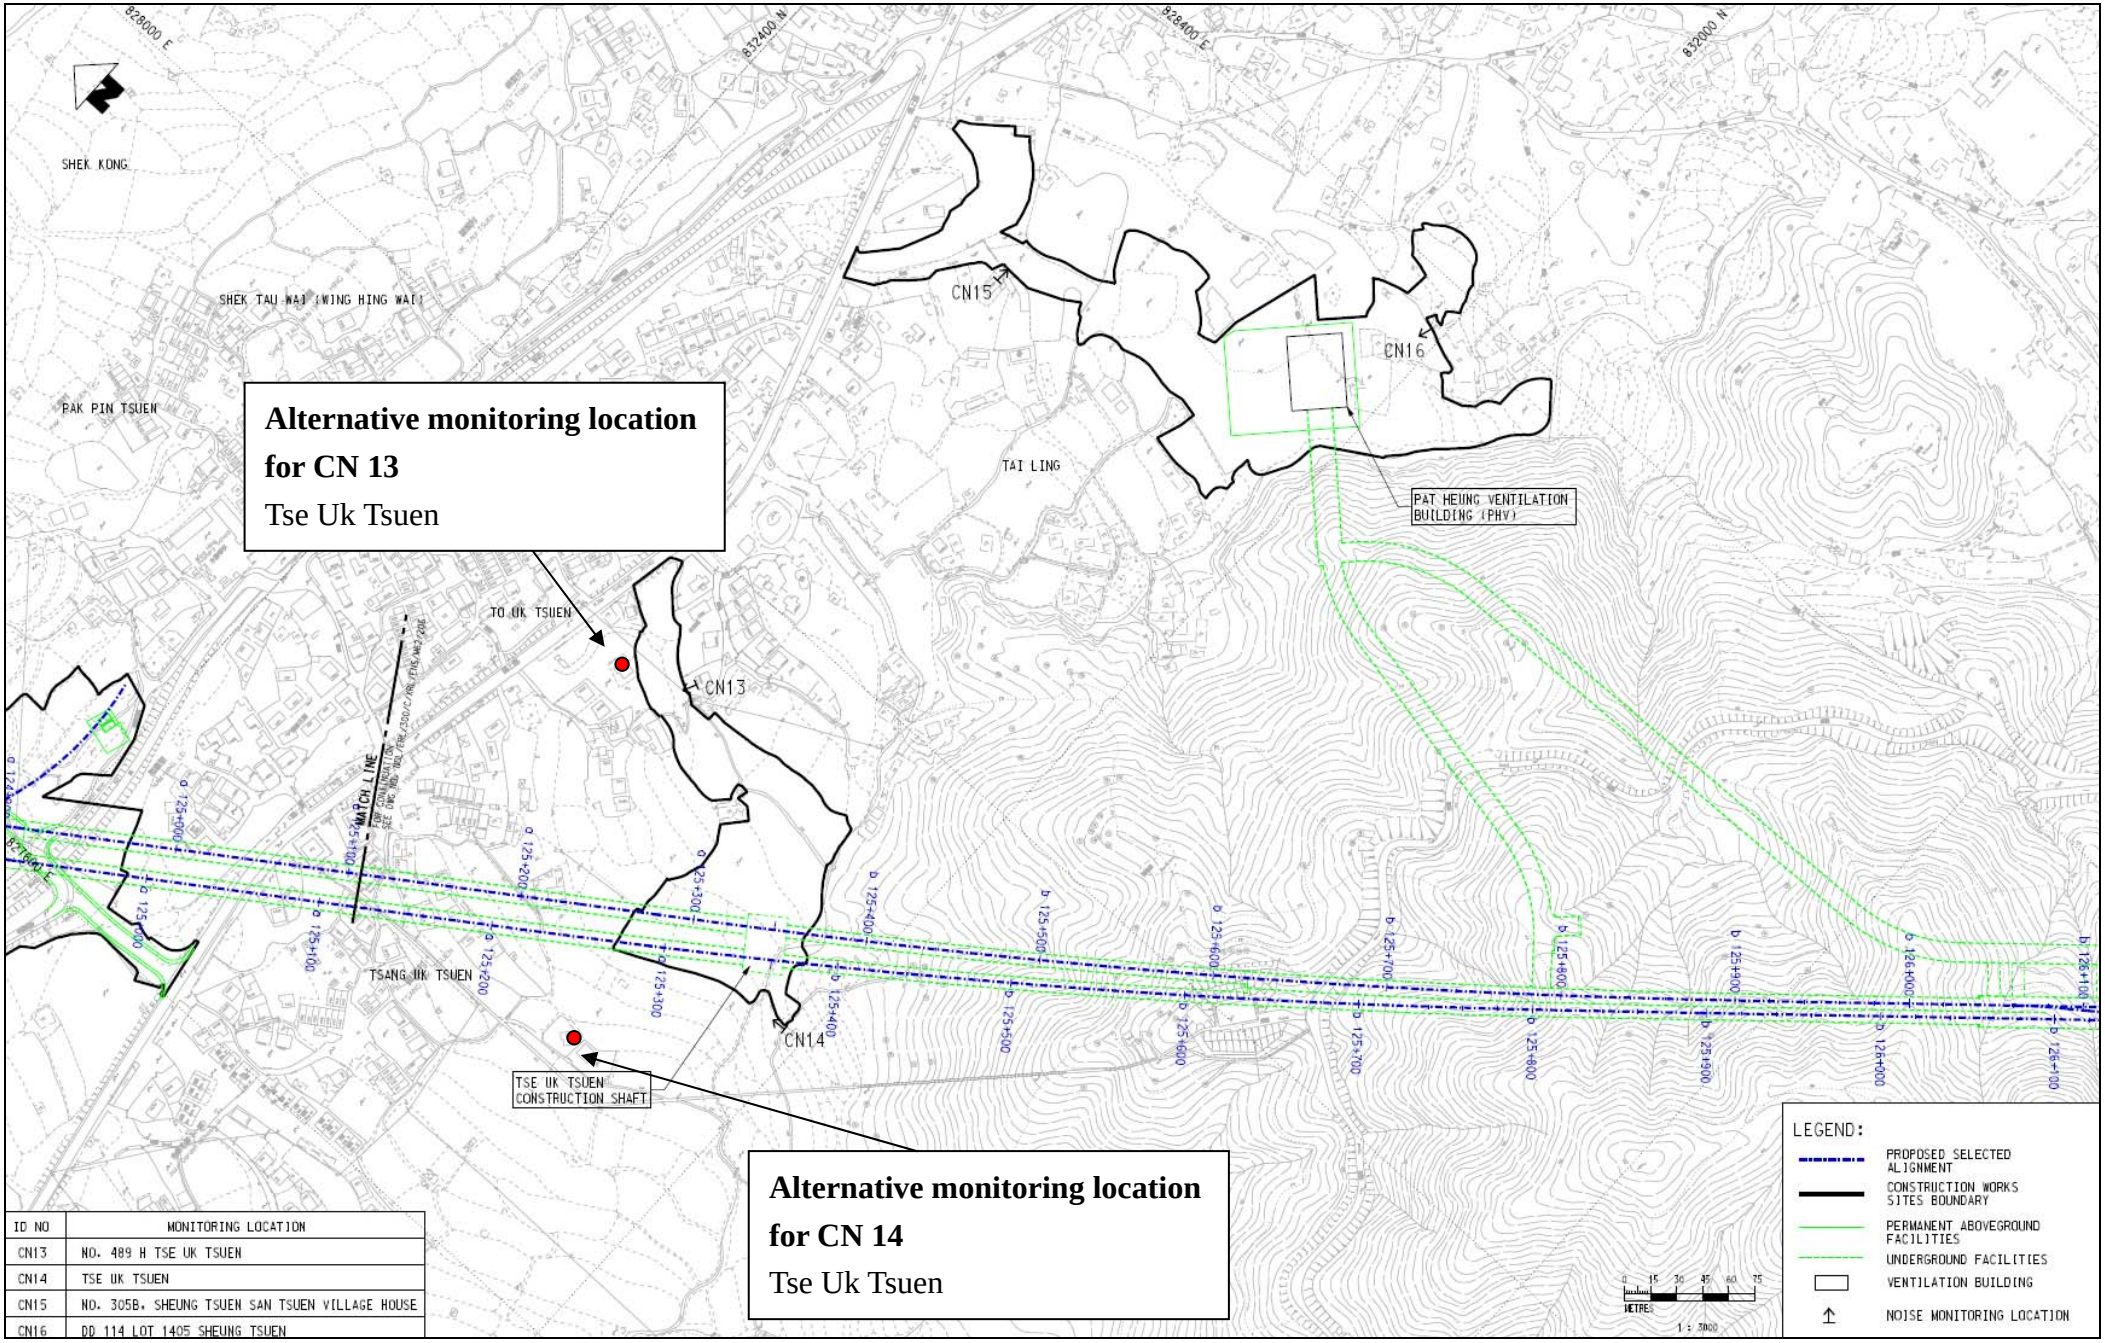

ID NO	MONITORING LOCATION
CN13	NO. 489 H TSE UK TSUEN
CN14	TSE UK TSUEN
CN15	NO. 305B, SHEUNG TSUEN SAN TSUEN VILLAGE HOUSE
CN16	DD 114 LOT 1405 SHEUNG TSUEN

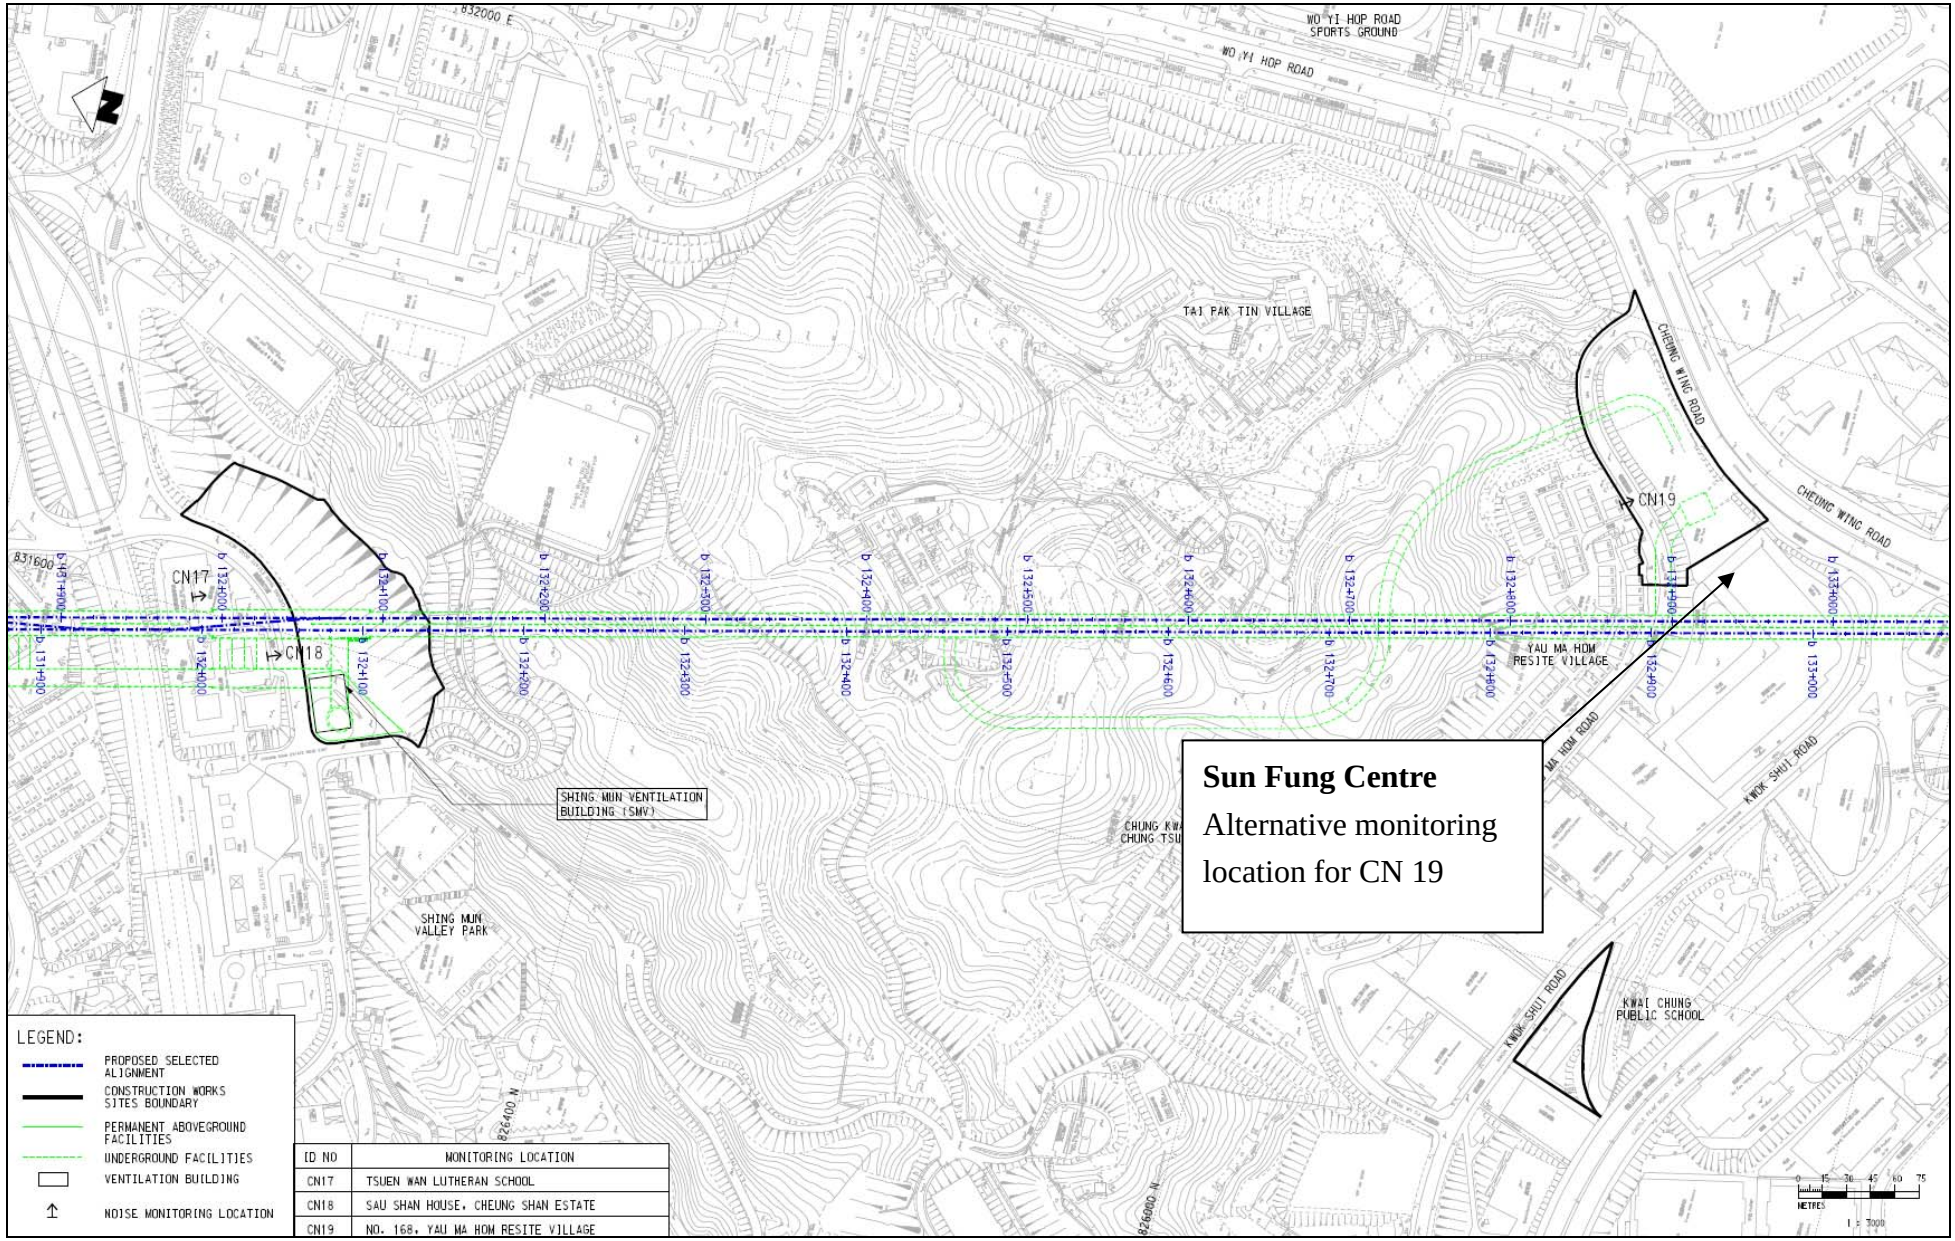
832000 E
WO YI HOP ROAD SPORTS GROUND
WO YI HOP ROAD
TAI PAK TIN VILLAGE
CHEUNG WING ROAD
CHEUNG WING ROAD
CN19
CN17
CN18
831600
SHING MUN VENTILATION BUILDING (SMV)
SHING MUN VALLEY PARK
YAU MA HOM RESITE VILLAGE
MA HOM ROAD
KWOK SHUI ROAD
KWOK SHUI ROAD
KWAI CHUNG PUBLIC SCHOOL
826400 N
826000 N
METRES
1 : 7000
Sun Fung Centre
Alternative monitoring location for CN 19
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
NOISE MONITORING LOCATION
ID NO | MONITORING LOCATION
CN17 | TSUEN WAN LUTHERAN SCHOOL
CN18 | SAU SHAN HOUSE, CHEUNG SHAN ESTATE
CN19 | NO. 168, YAU MA HOM RESITE VILLAGE



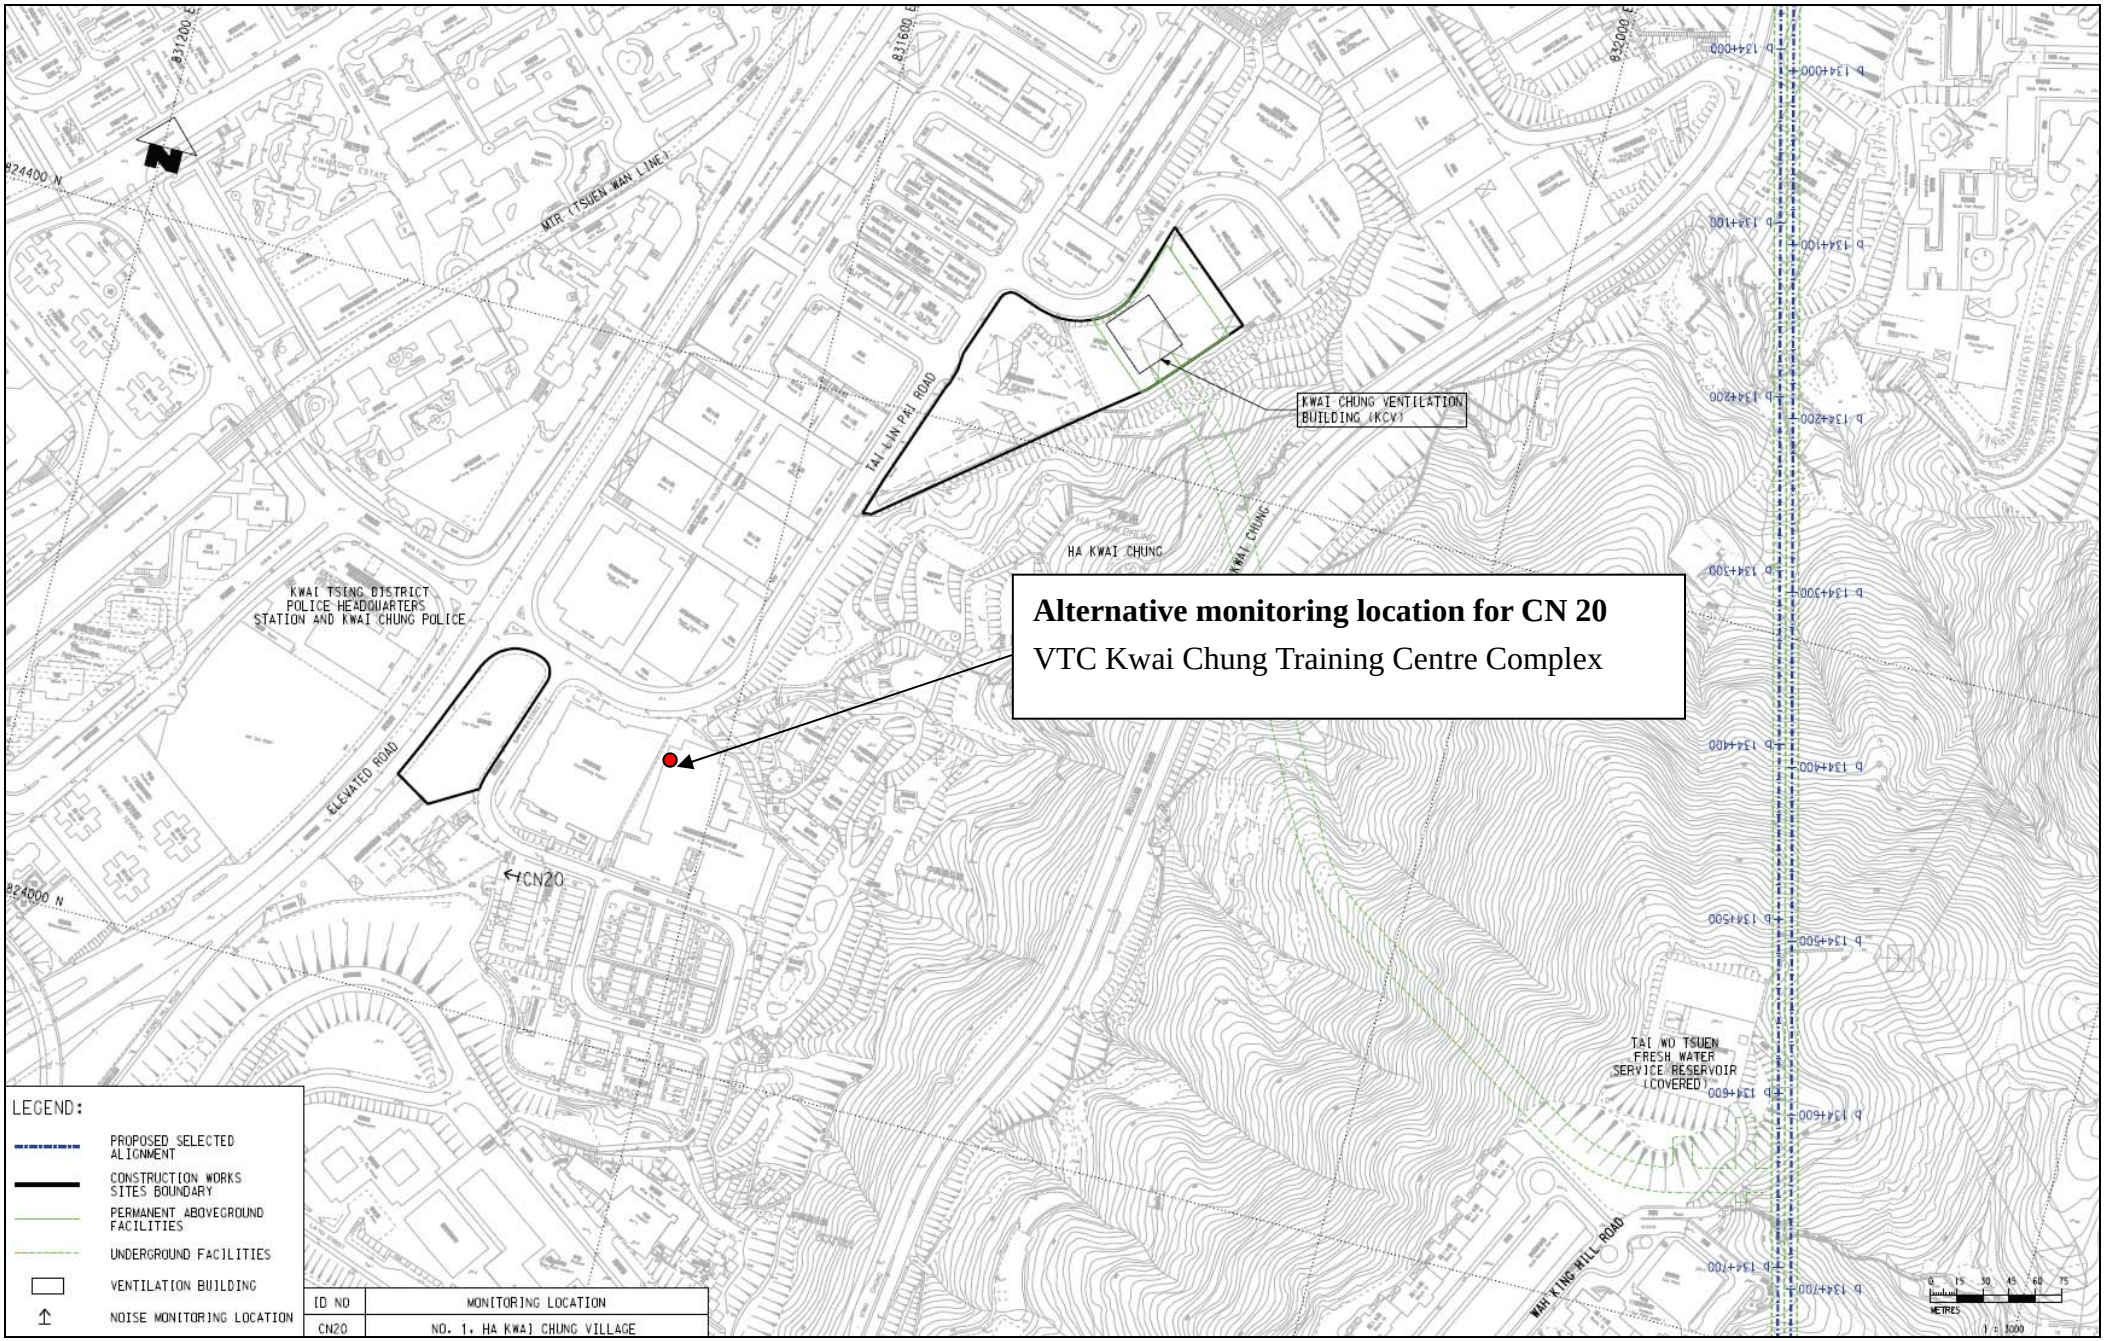



Figure 3 – Noise Monitoring Location

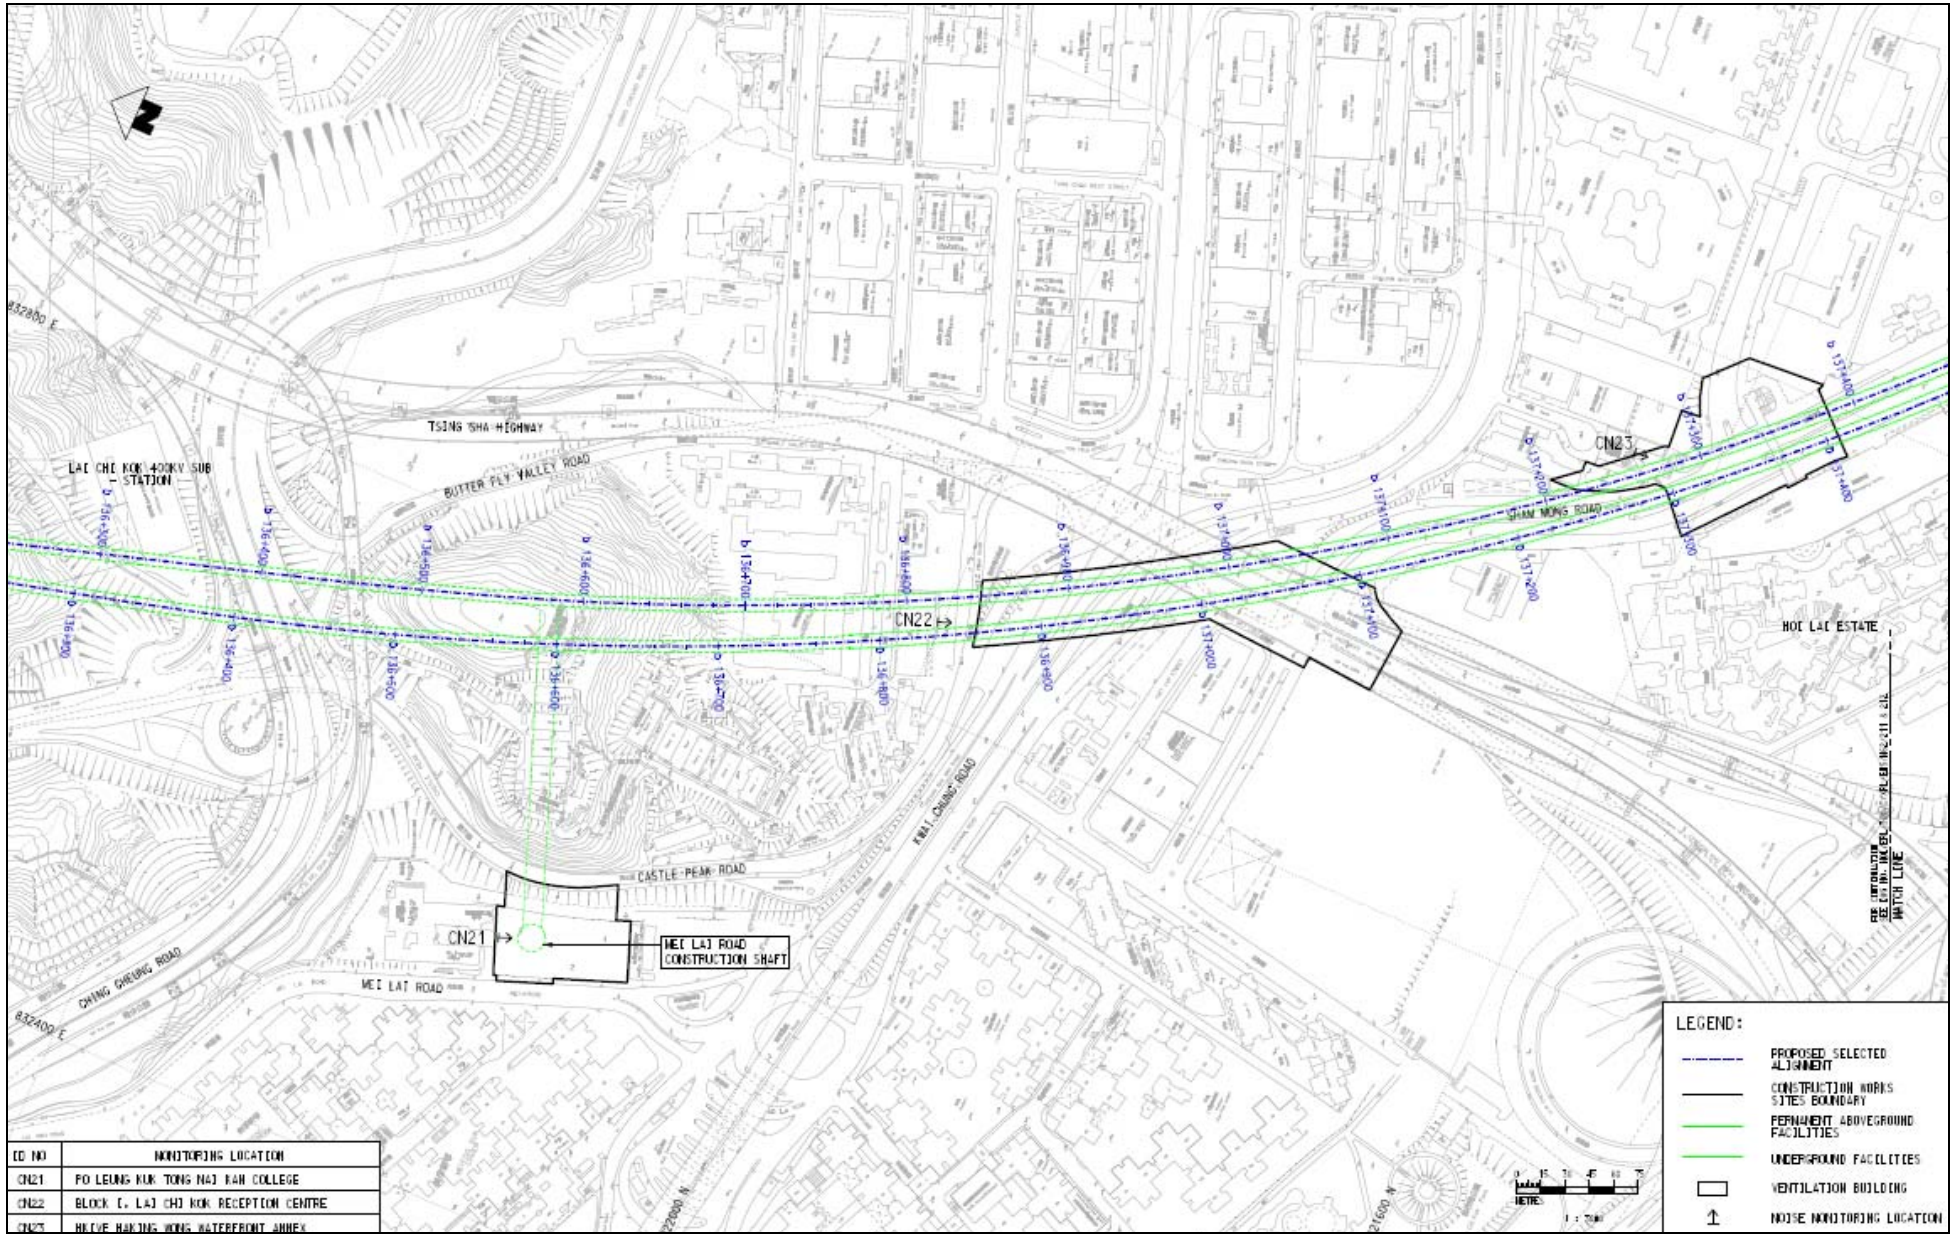


ID NO	MONITORING LOCATION
CN21	PO LEUNG KUK TONG NAI RAN COLLEGE
CN22	BLOCK C, LAI CHI KOK RECEPTION CENTRE
CN23	HOLYE HAKKING WONG WATERFRONT ANNEX

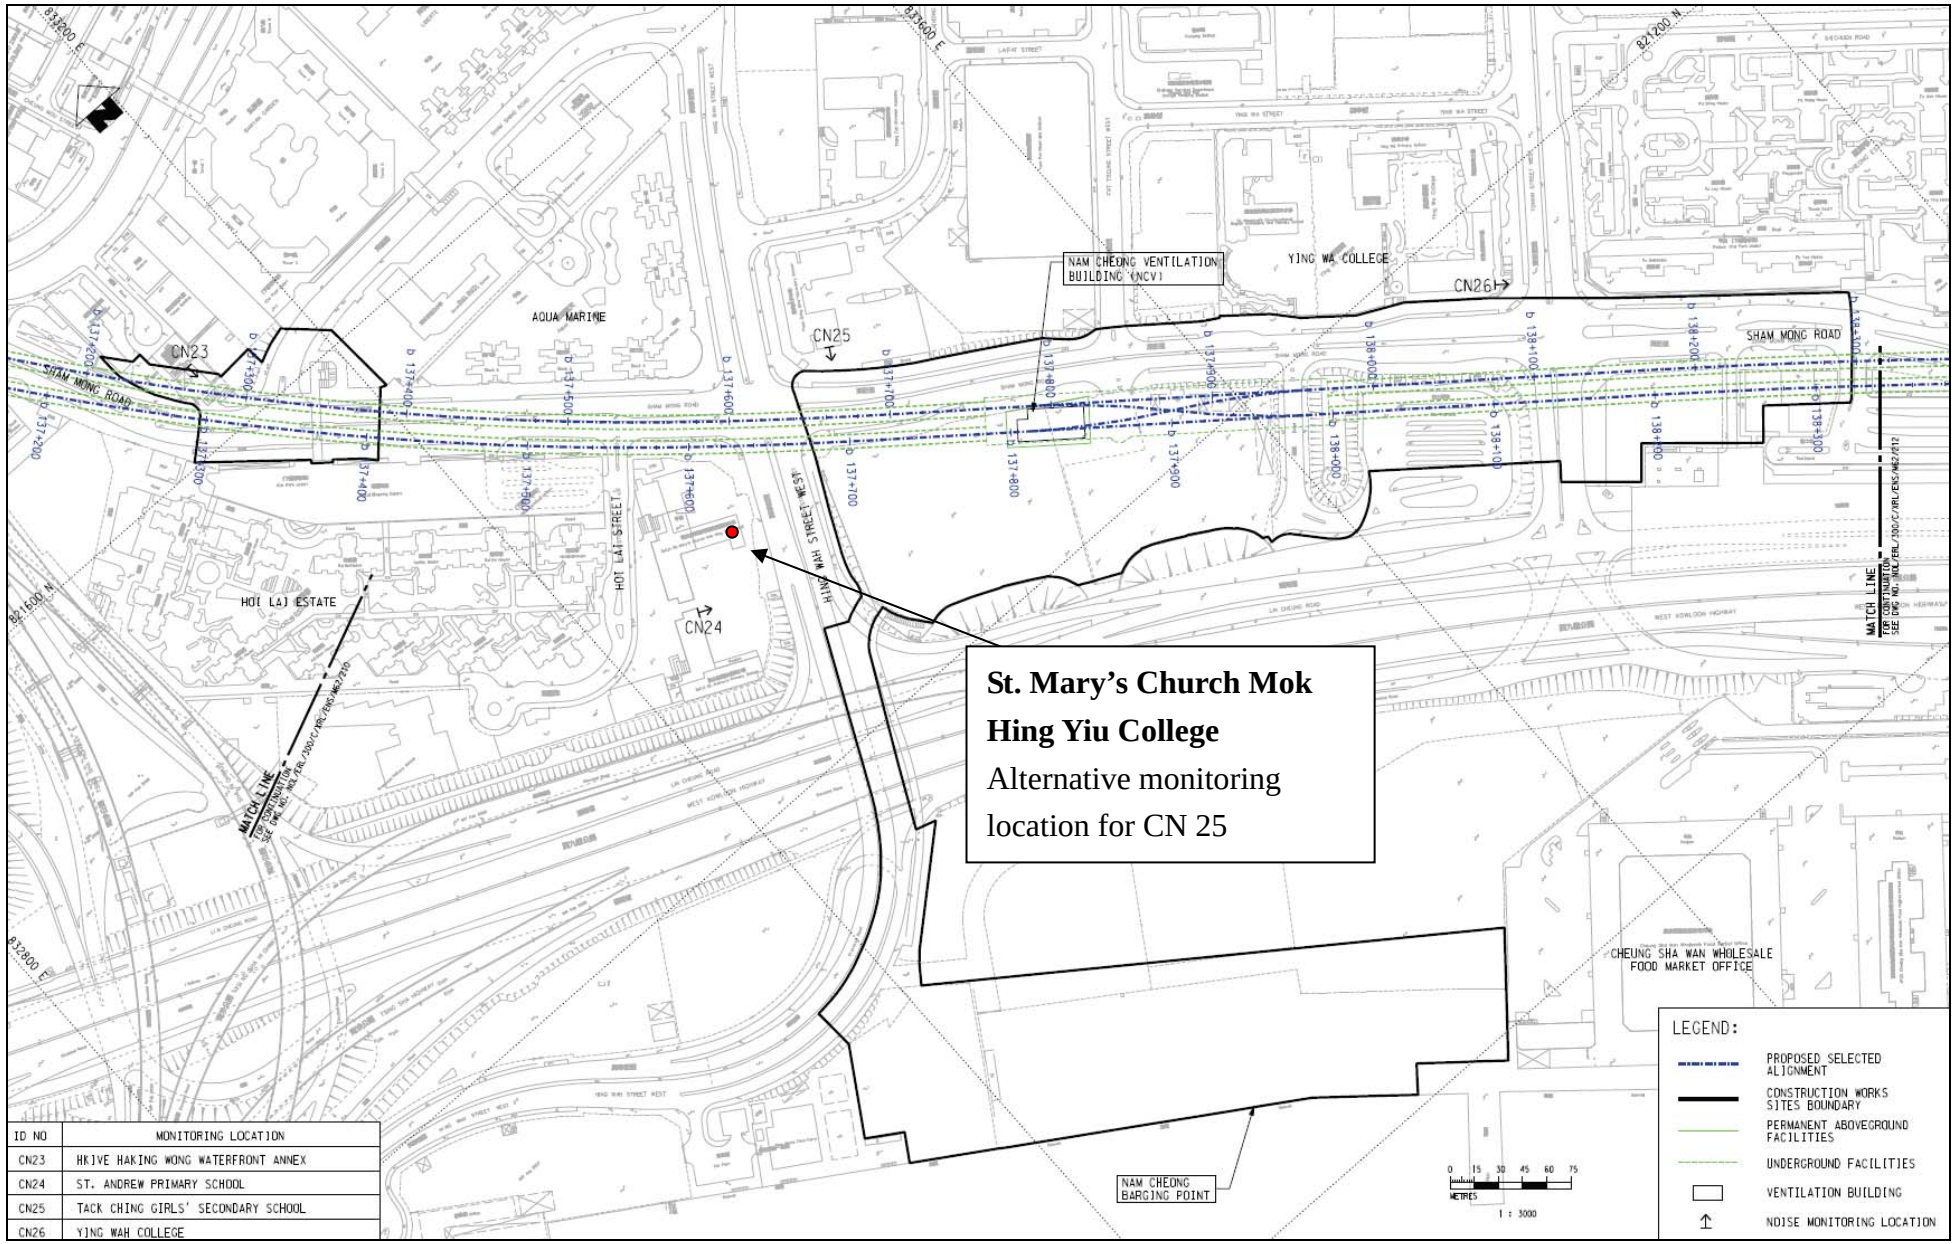


ID NO	MONITORING LOCATION
CN23	HKIVE HAKING WONG WATERFRONT ANNEX
CN24	ST. ANDREW PRIMARY SCHOOL
CN25	TACK CHING GIRLS' SECONDARY SCHOOL
CN26	YING WAH COLLEGE

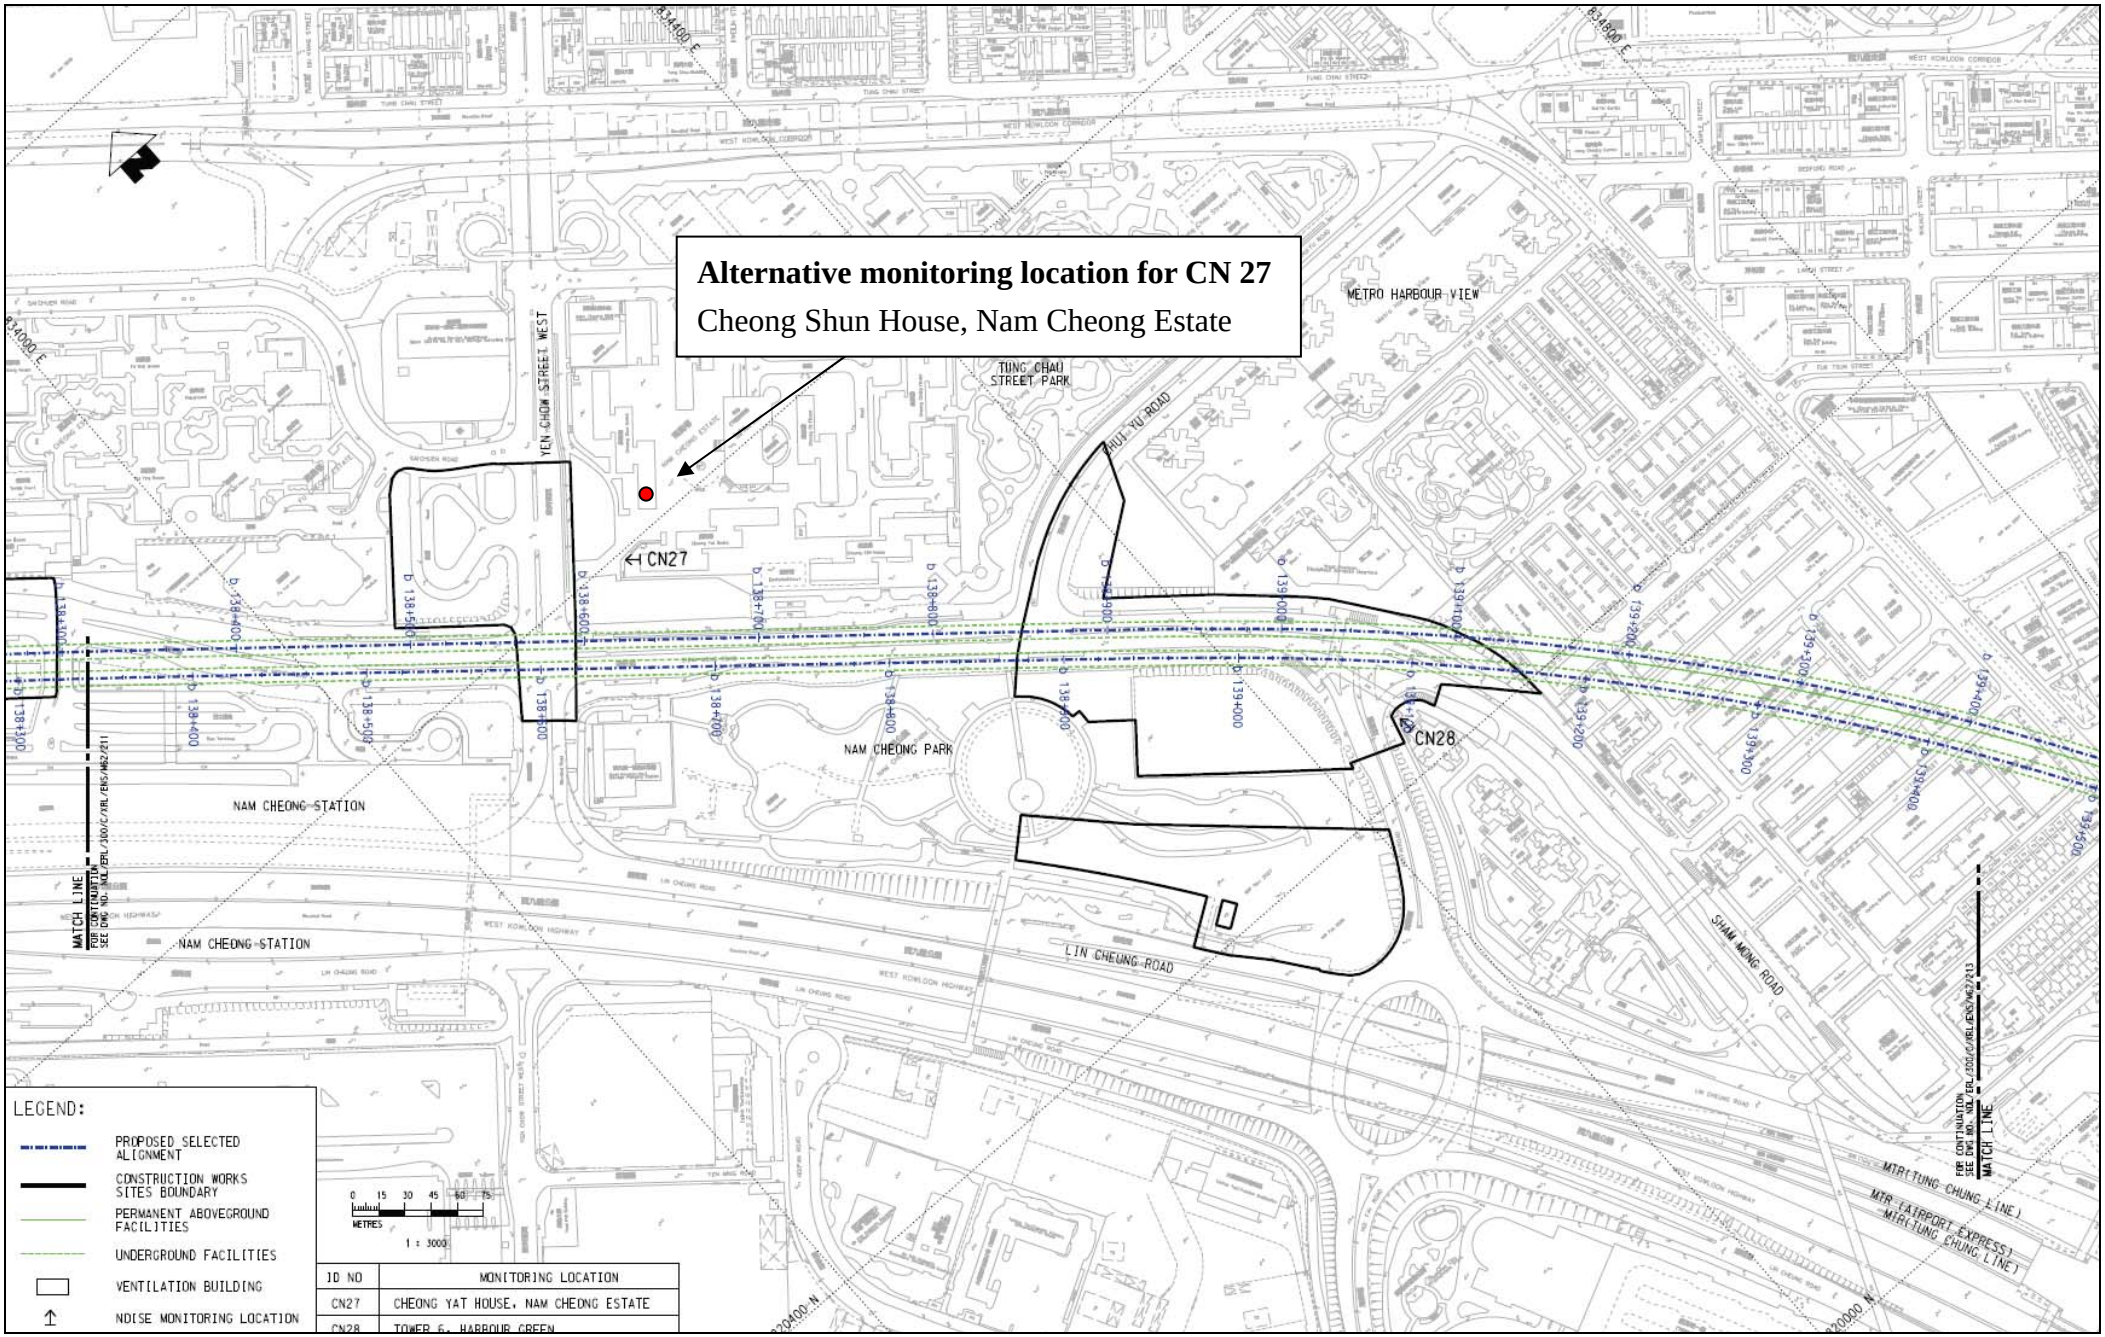

Alternative monitoring location for CN 27
Cheong Shun House, Nam Cheong Estate
CN27
CN28
NAM CHEONG PARK
NAM CHEONG STATION
NAM CHEONG STATION
TUNG CHAU STREET PARK
METRO HARBOUR VIEW
YEN CHOW STREET WEST
HUI YU ROAD
LIN CHEUNG ROAD
SHAM MONG ROAD
WEST KOWLOON HIGHWAY
MATCH LINE
FOR CONTINUATION SEE DWG NO. XOL/EBL/300/C/XRL/ENS/MW2/2411
MATCH LINE
FOR CONTINUATION SEE DWG NO. XOL/EBL/300/D/XRL/ENS/MW2/2413
MTR (TUNG CHUNG LINE)
MTR (AIRPORT EXPRESS)
MTR (TUNG CHUNG LINE)
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
NOISE MONITORING LOCATION
0 15 30 45 60 75
METRES
1 : 3000
ID NO
MONITORING LOCATION
CN27
CHEONG YAT HOUSE, NAM CHEONG ESTATE
CN28
TOWER 6, HARBOUR GREEN

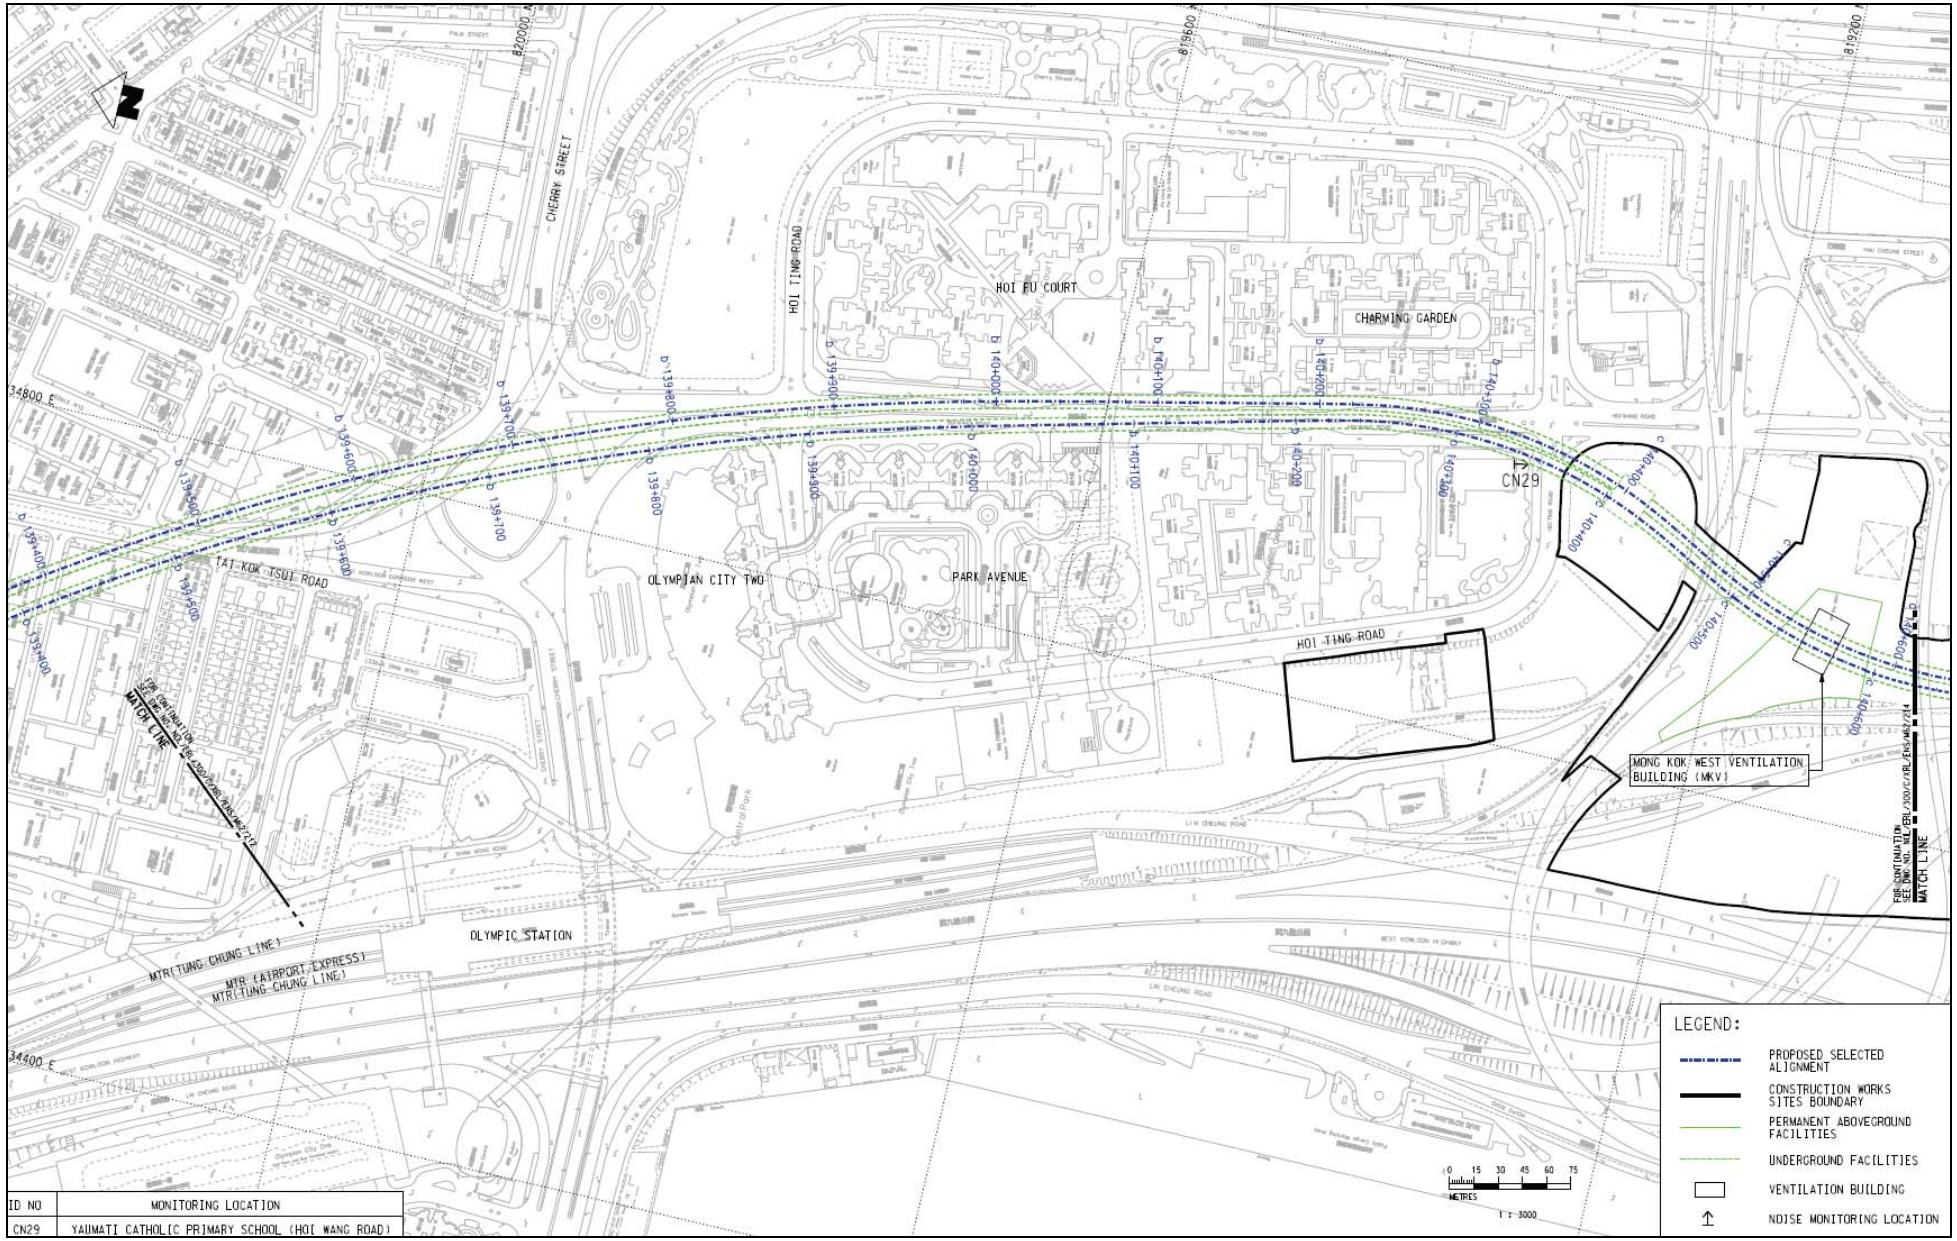



ID NO	MONITORING LOCATION
CN29	YAUMATI CATHOLIC PRIMARY SCHOOL (HOI WANG ROAD)

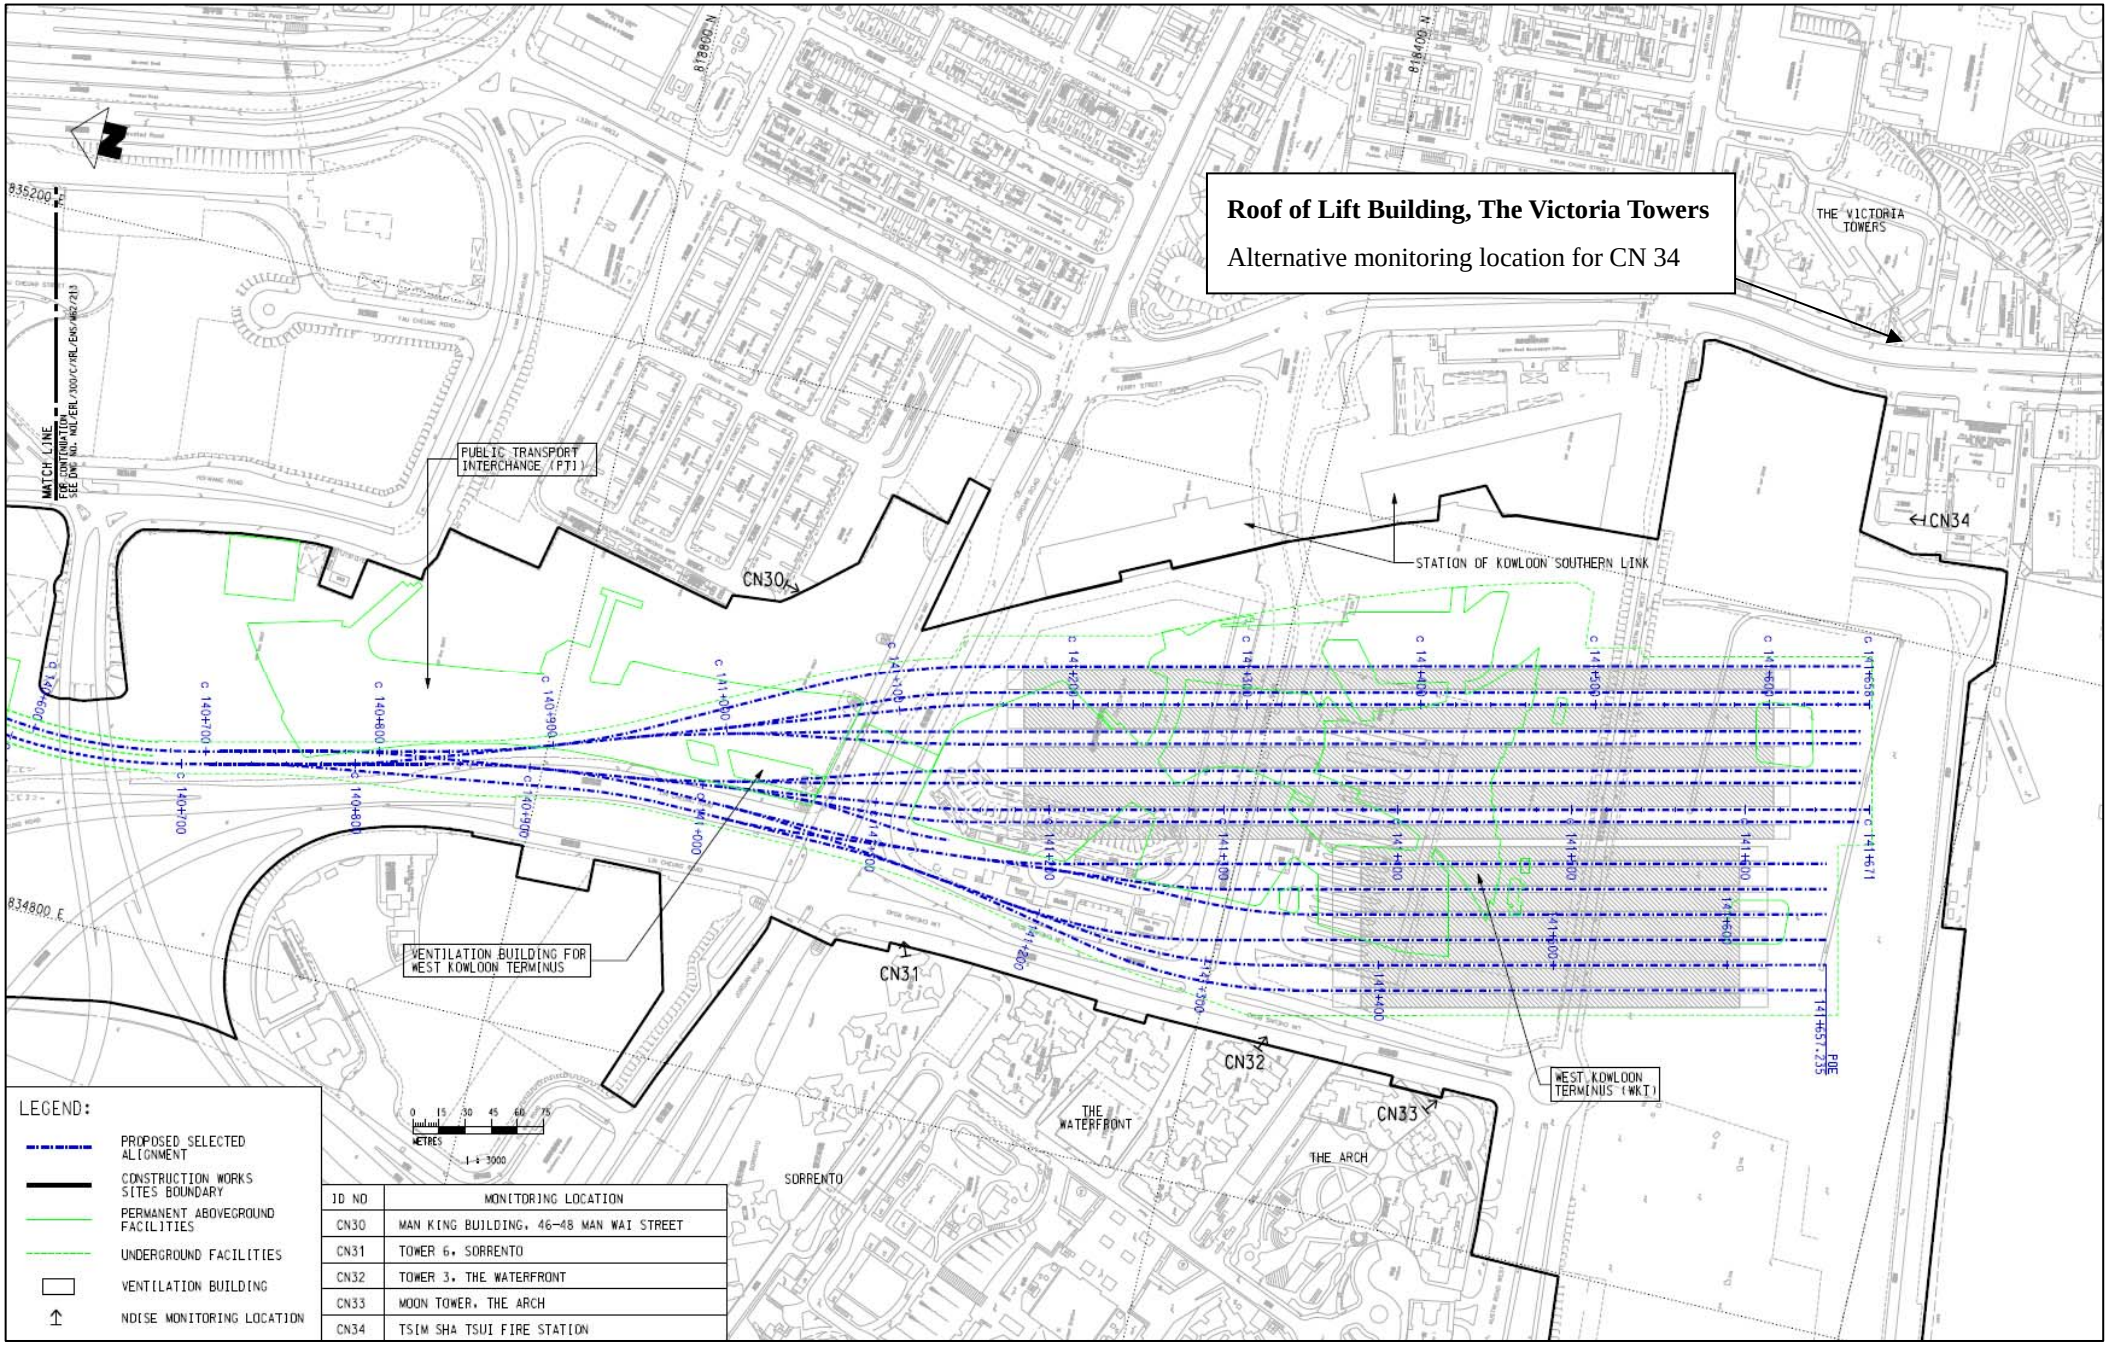



Noise monitoring locations

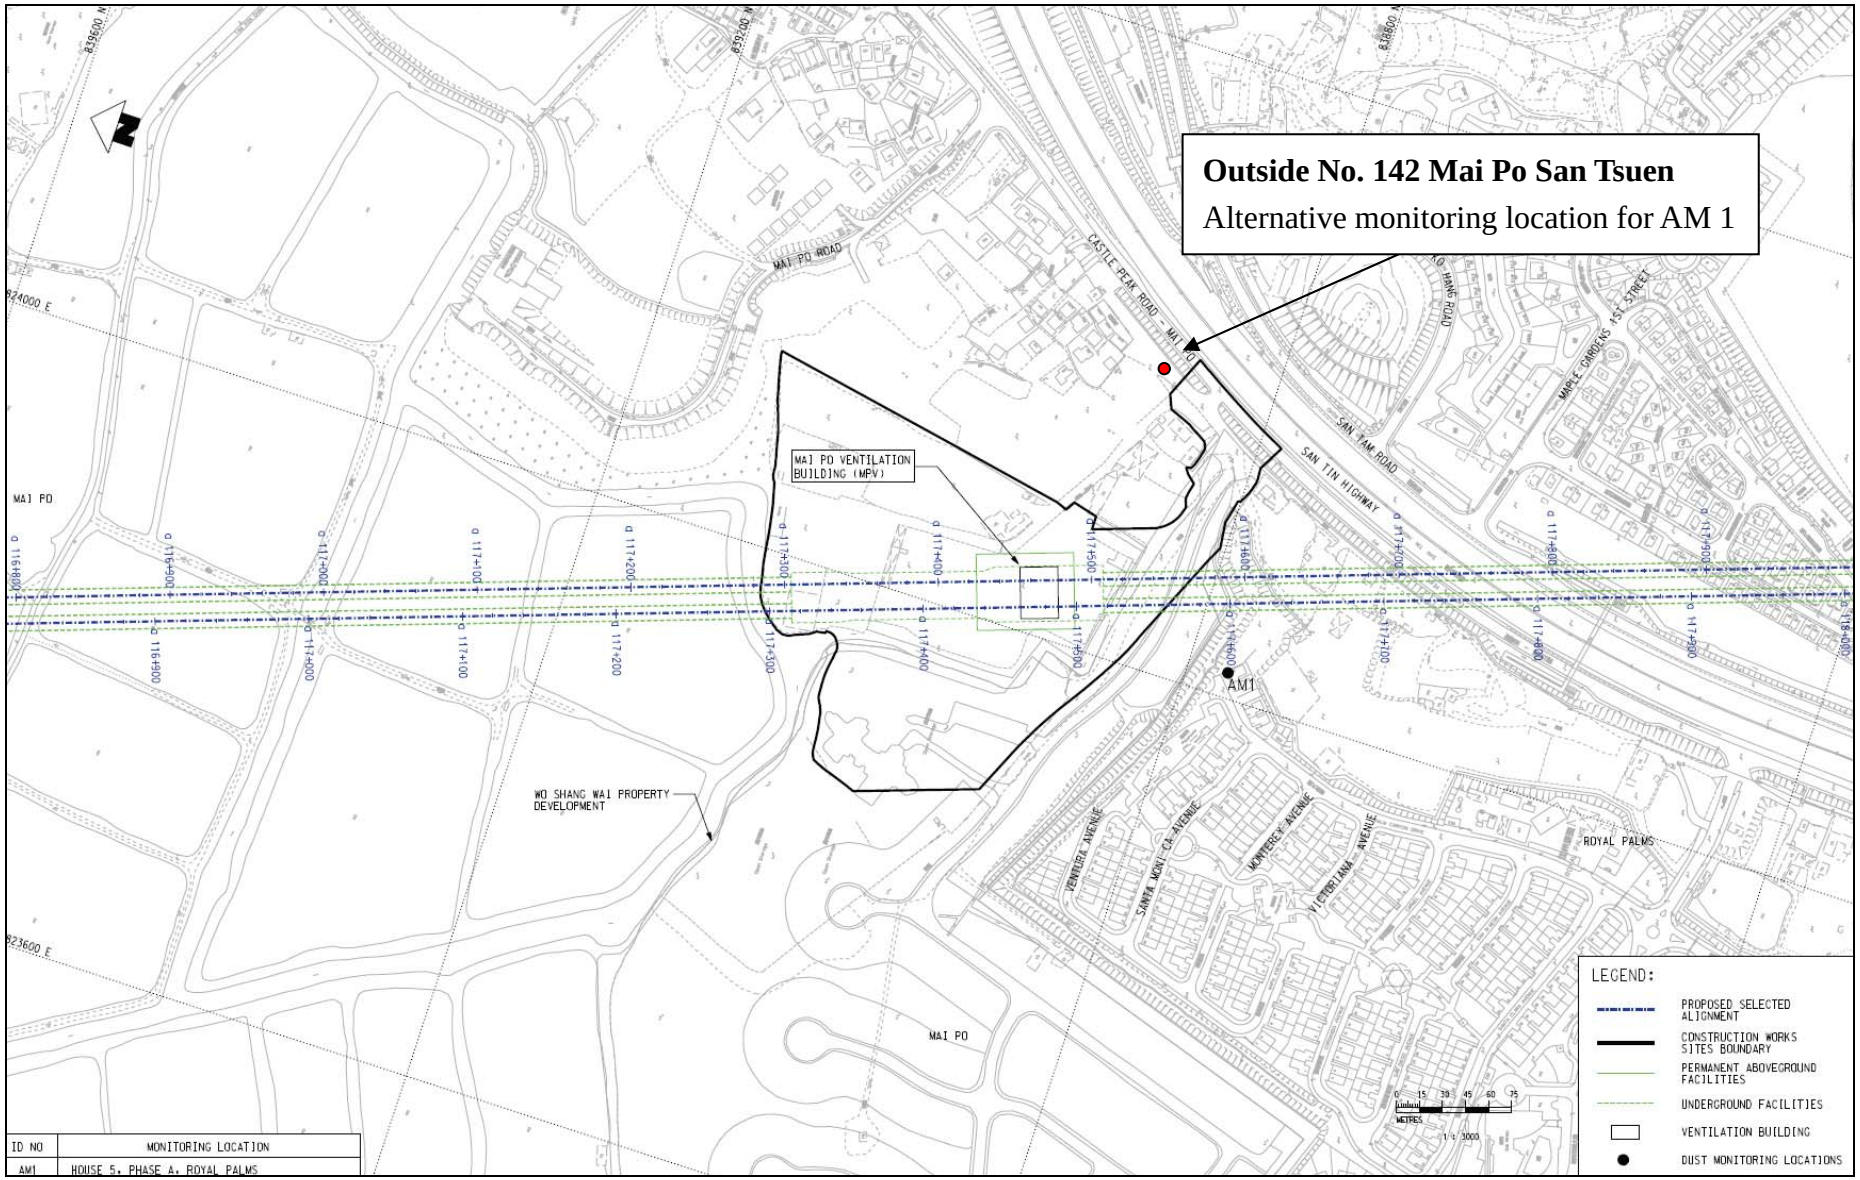
Outside No. 142 Mai Po San Tsuen
Alternative monitoring location for AM 1
MAI PO VENTILATION BUILDING (MPV)
WO SHANG WAI PROPERTY DEVELOPMENT
AM1
MAI PO
MAI PO ROAD
CASTLE PEAK ROAD - MAI PO
SAN TIN HIGHWAY
SAN TAM ROAD
ROYAL PALMS
VENTURA AVENUE
SANTA MONICA AVENUE
MONTEREY AVENUE
VICTORIANA AVENUE
MARIE CURIENS 1ST STREET
839600 N
824000 E
823600 E
ID NO
MONITORING LOCATION
AM1
HOUSE 5, PHASE 4, ROYAL PALMS
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATIONS
METRES
1 : 3000

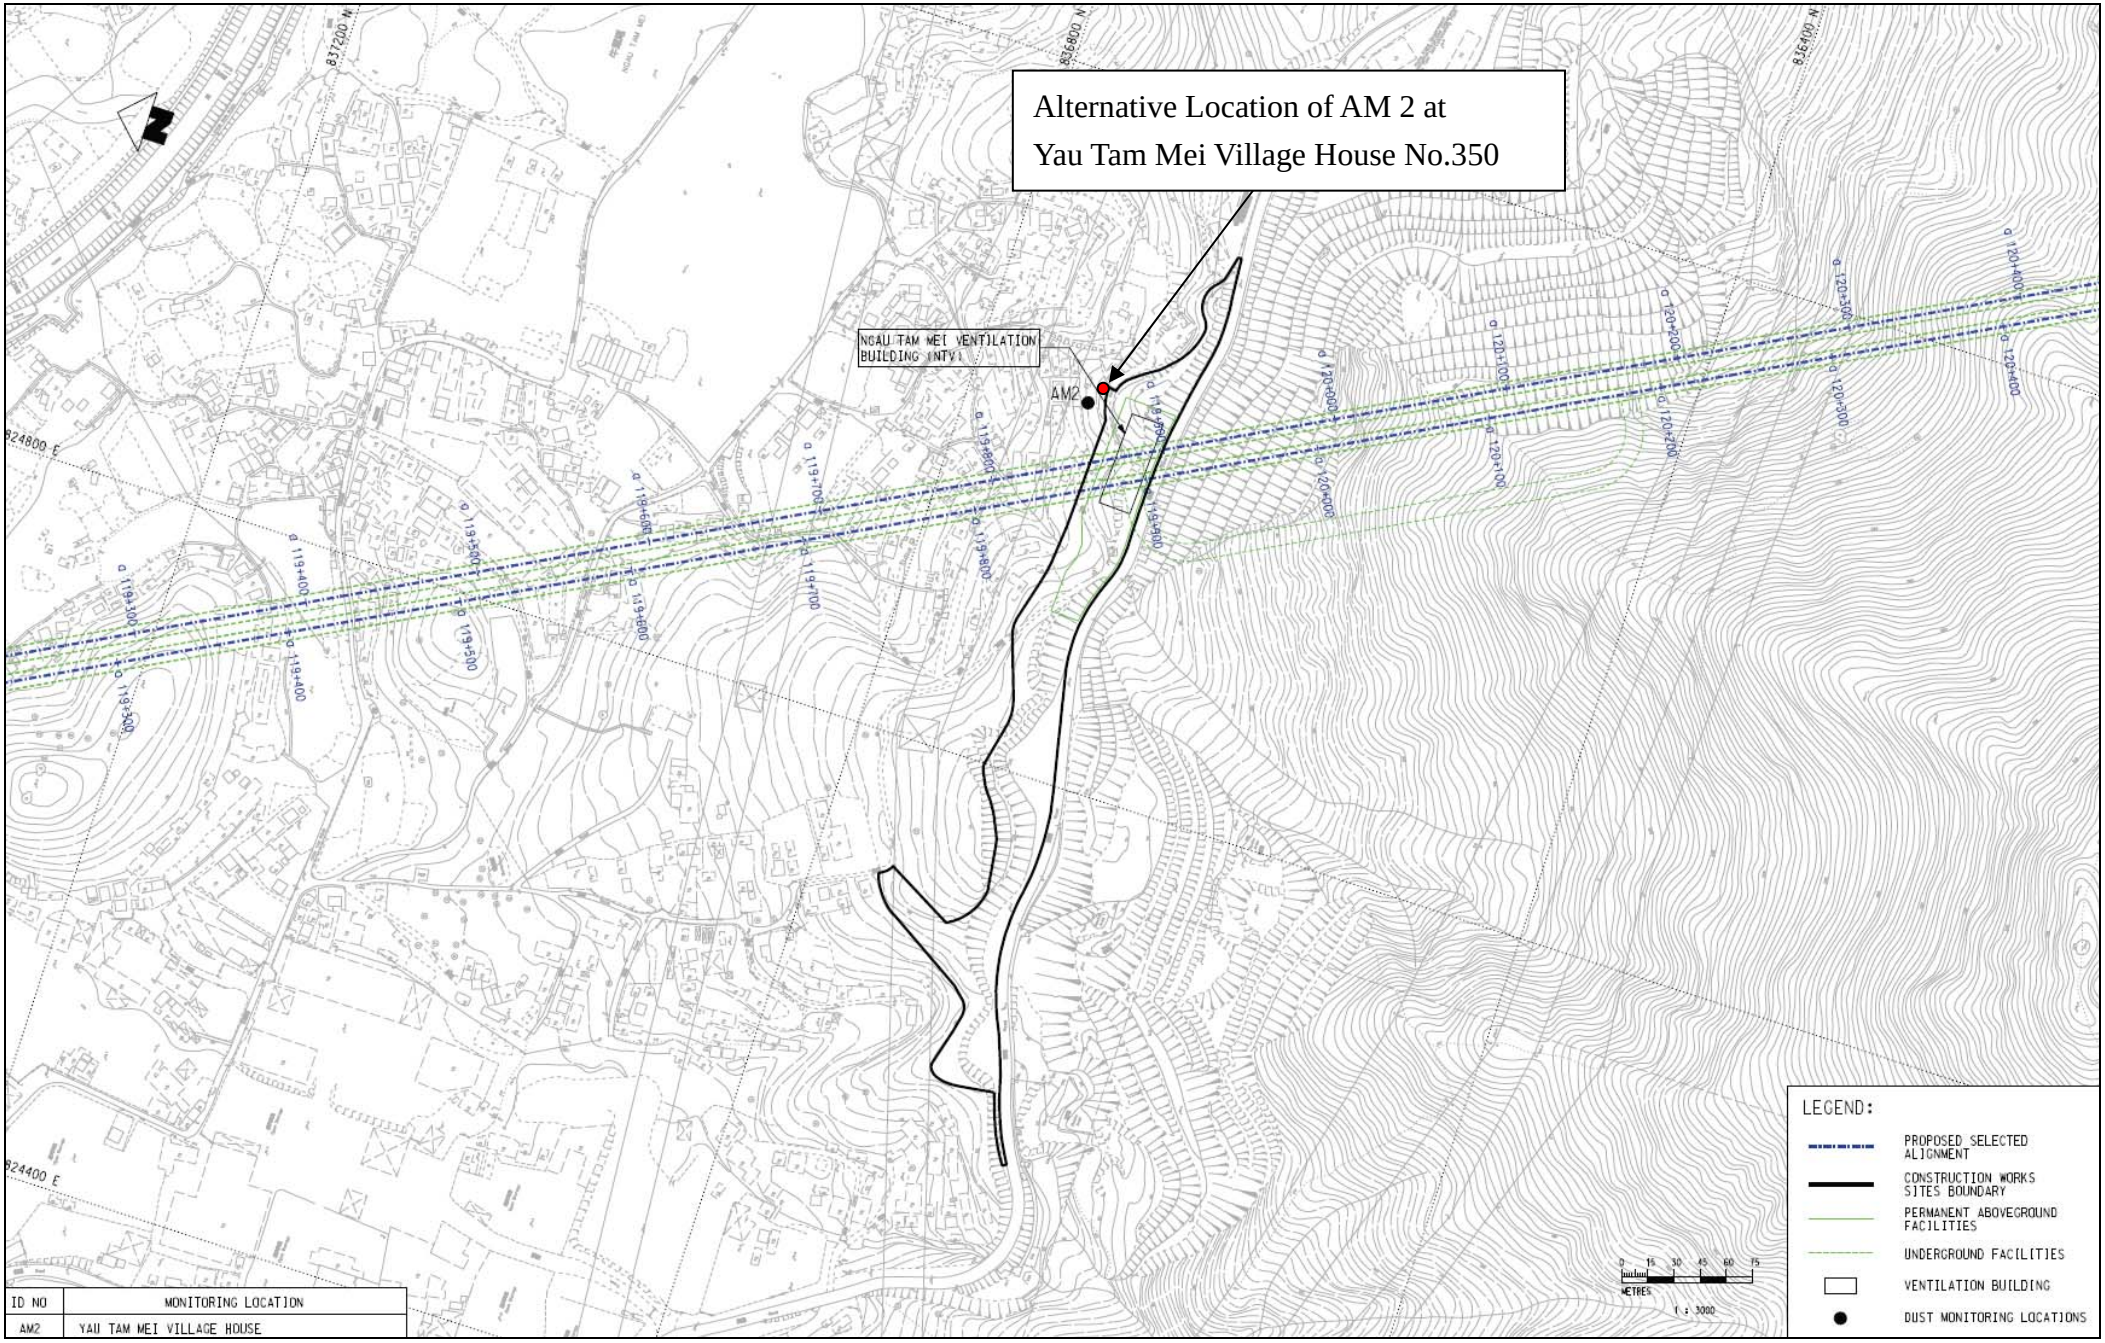

Alternative Location of AM 2 at
Yau Tam Mei Village House No.350
NGAU TAM MEI VENTILATION BUILDING (NTV)
AM2
837200 N
836800 N
836400 N
824800 E
824400 E
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATIONS
METRES
1 : 3000
ID NO | MONITORING LOCATION
AM2 | YAU TAM MEI VILLAGE HOUSE

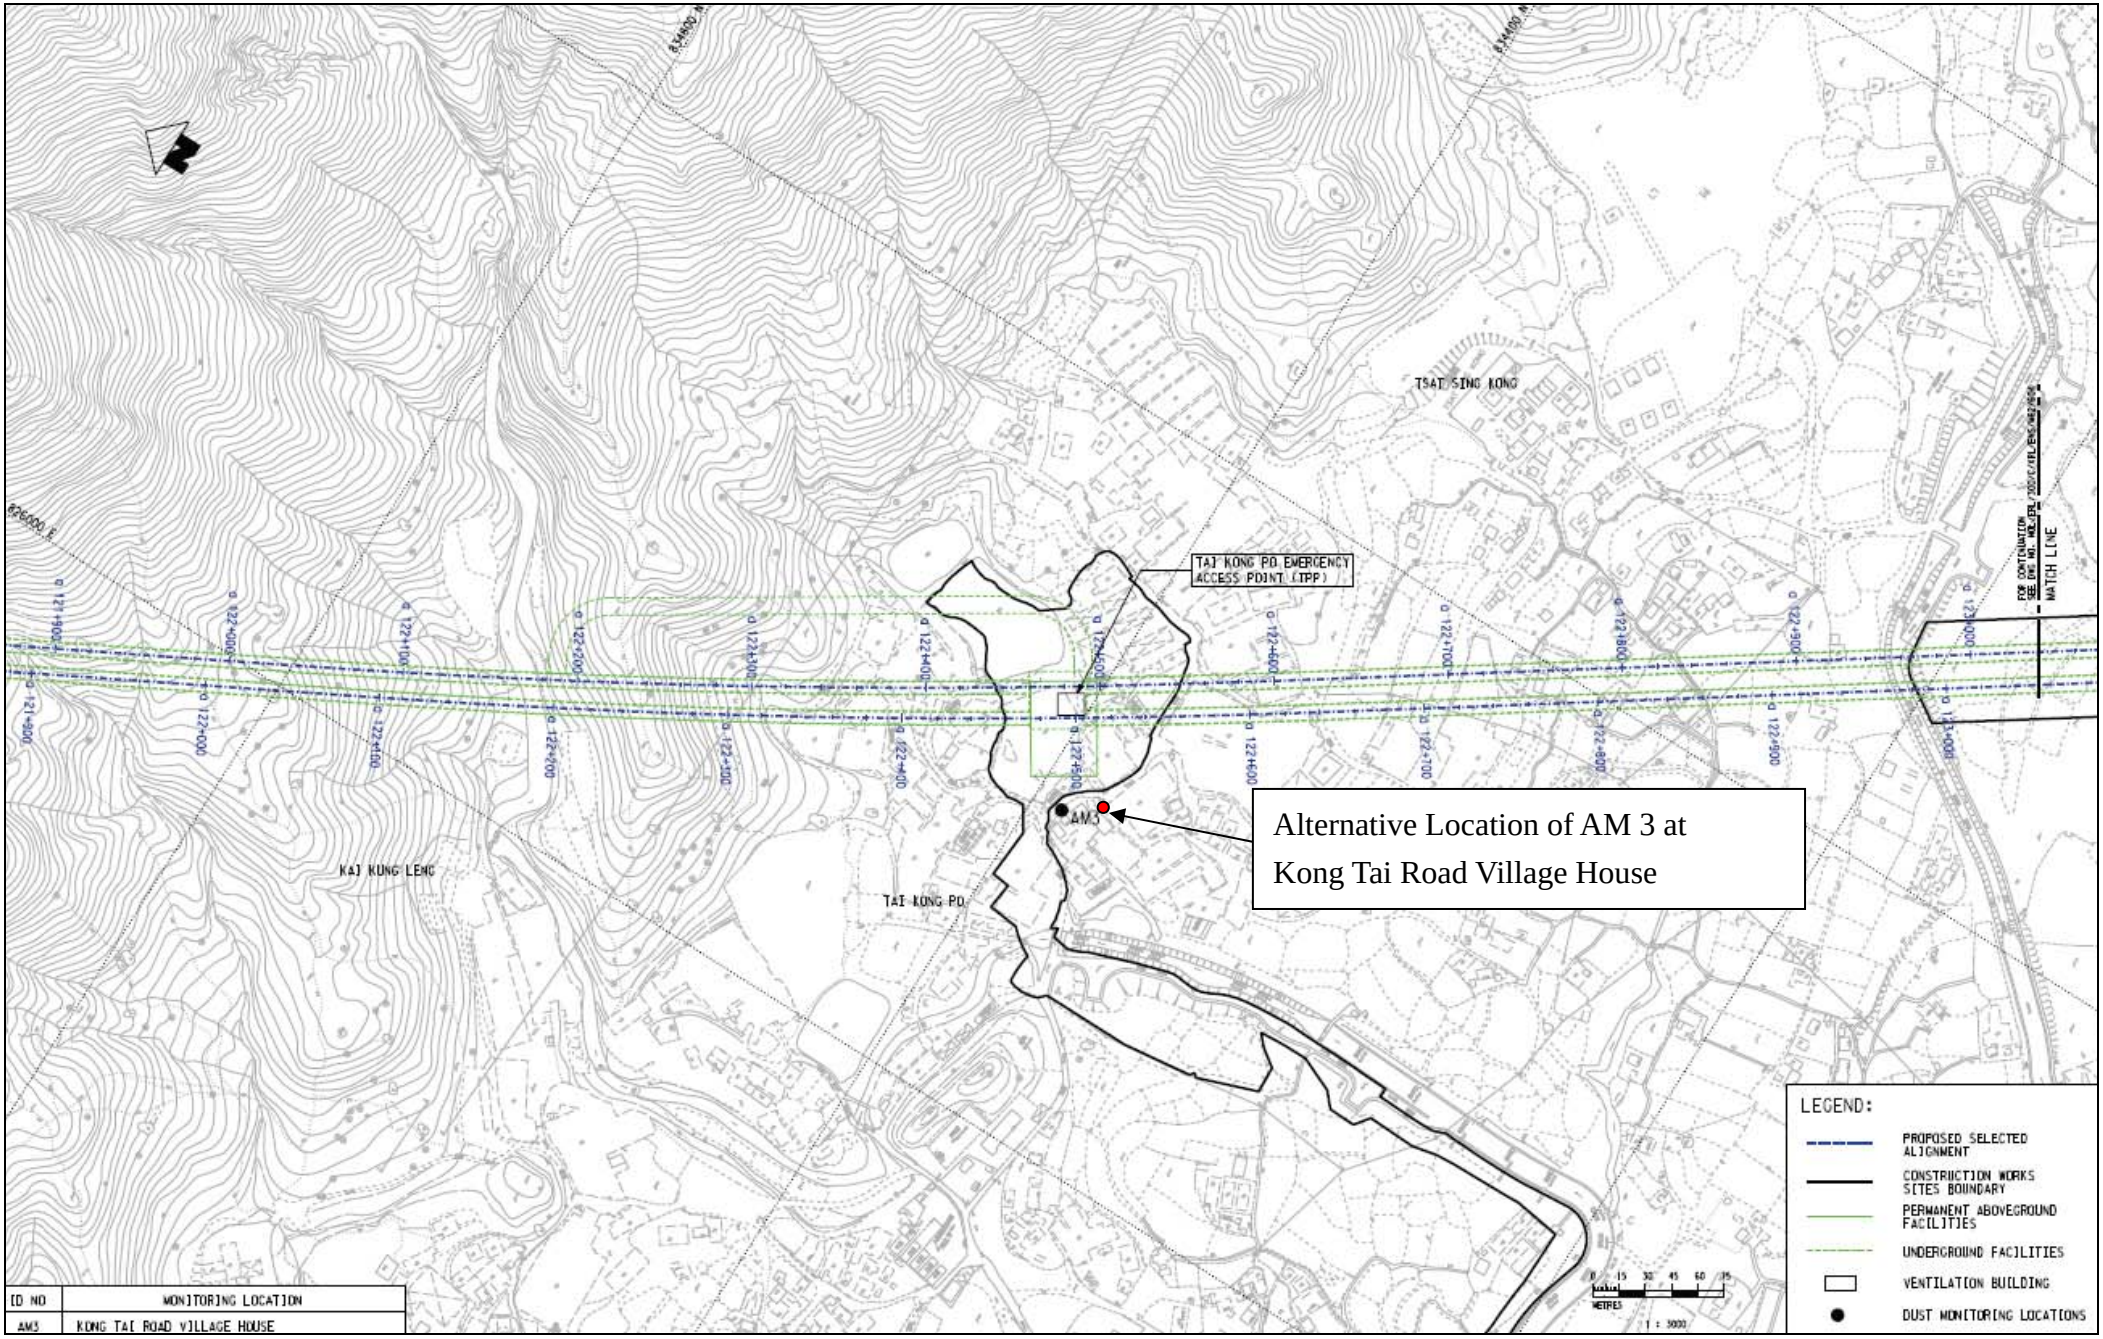

TSAT SING KONG
TAI KONG PO EMERGENCY ACCESS POINT (TPP)
AM3
Alternative Location of AM 3 at Kong Tai Road Village House
KAI KONG LENG
TAI KONG PO
MATCH LINE
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATIONS
ID NO
MONITORING LOCATION
AM3
KONG TAI ROAD VILLAGE HOUSE

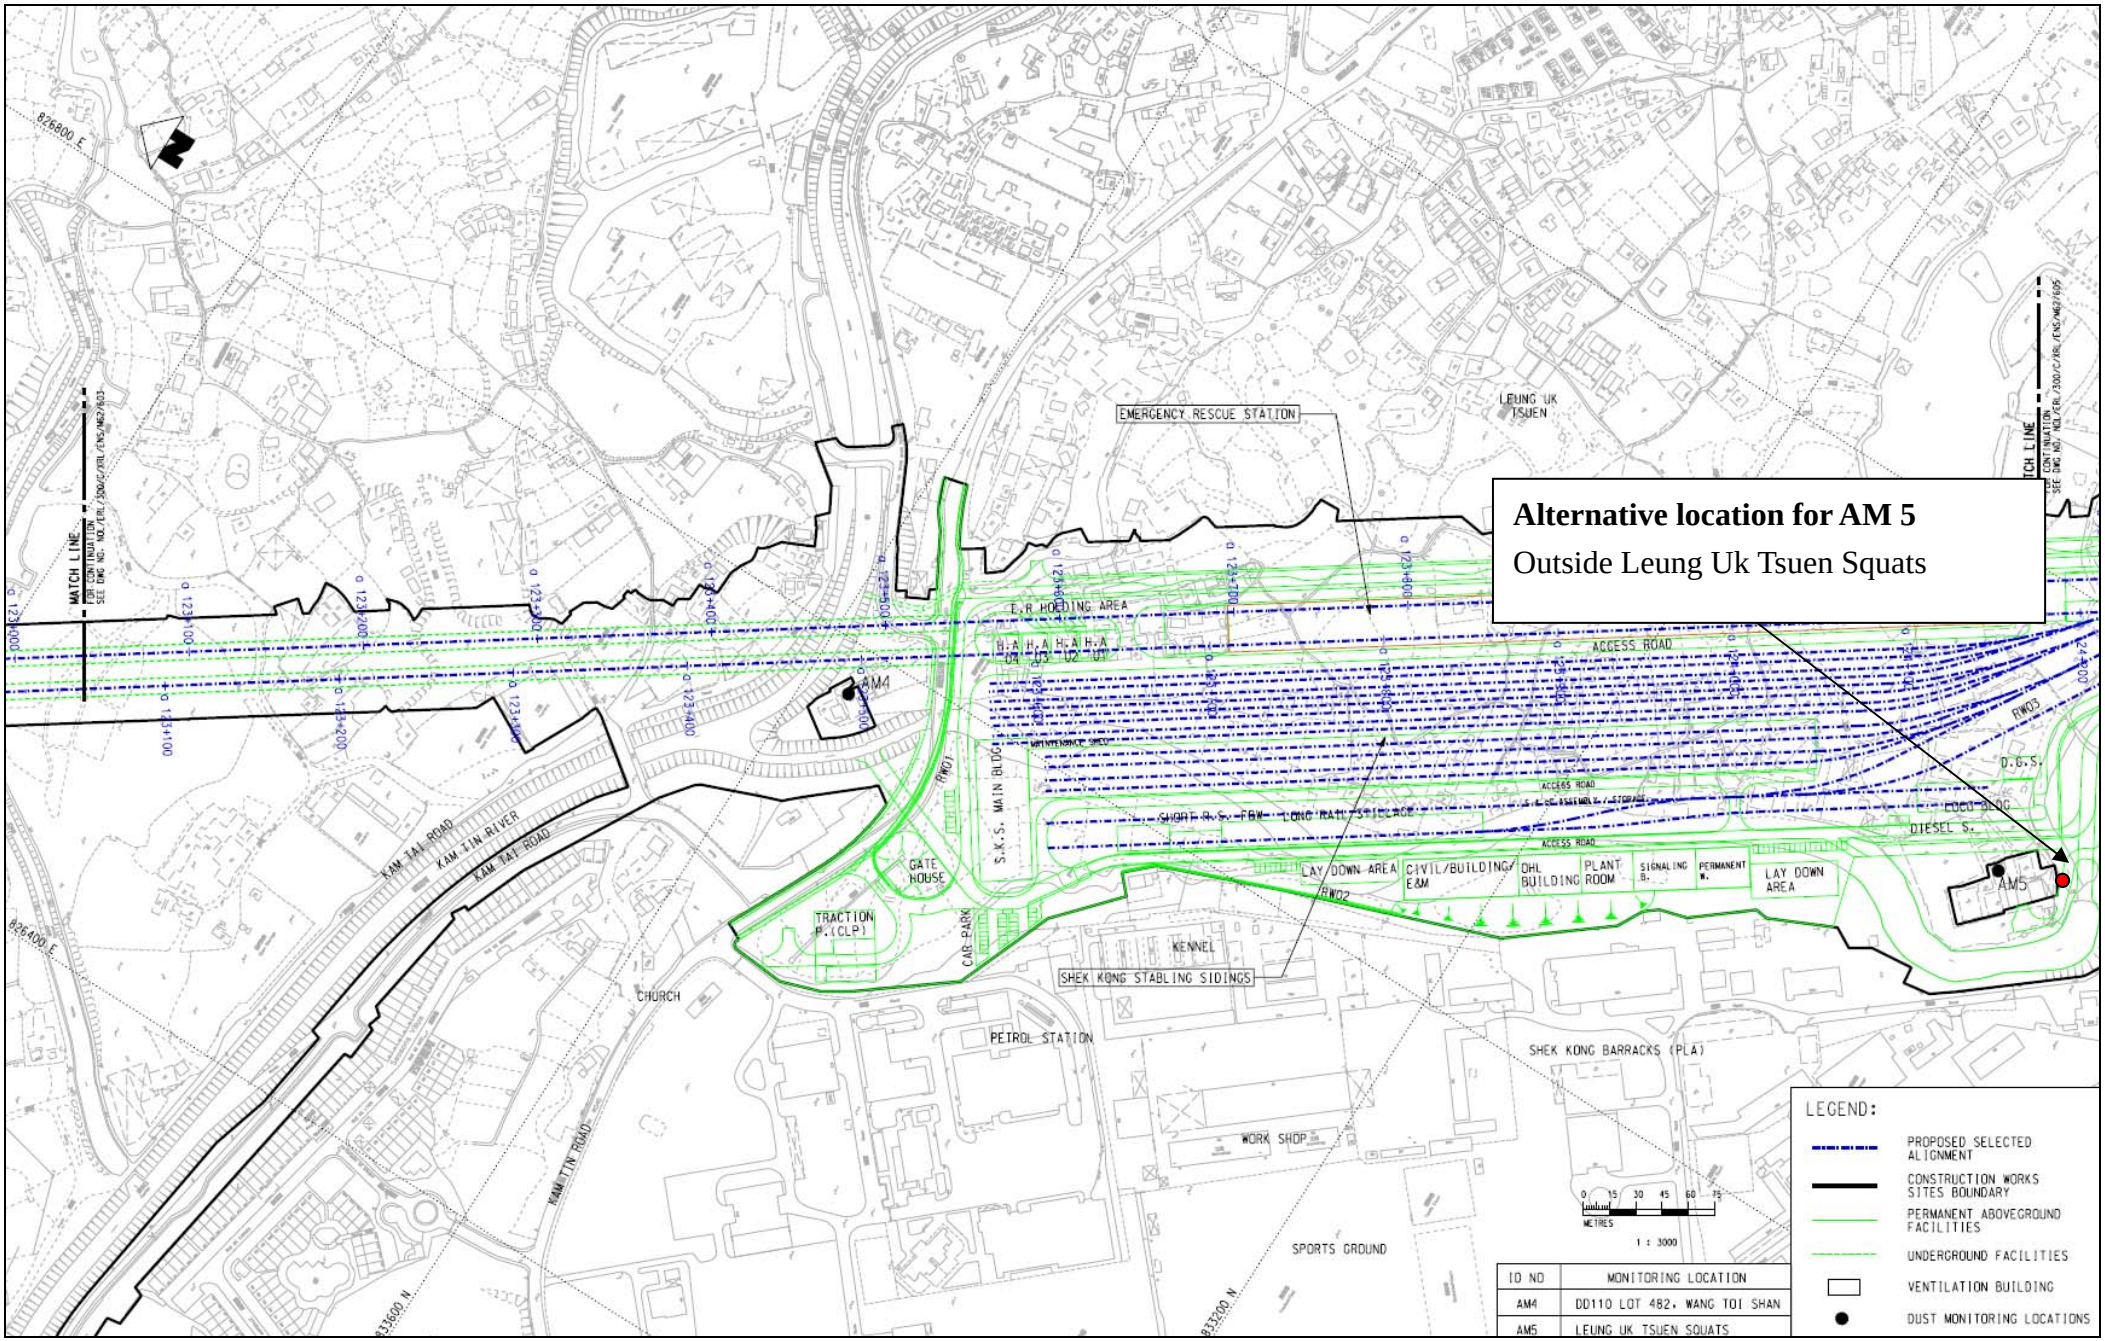
Alternative location for AM 5
Outside Leung Uk Tsuen Squats
EMERGENCY RESCUE STATION
LEUNG UK TSUEN
MATCH LINE
ACCESS ROAD
T.R HOEDING AREA
AM4
AM5
S.K.S. MAIN BLDG.
GATE HOUSE
TRACTION P.(CLP)
CAR PARK
KENNEL
SHEK KONG STABLING SIDINGS
CHURCH
PETROL STATION
WORK SHOP
SHEK KONG BARRACKS (PLA)
SPORTS GROUND
KAM TAI ROAD
KAM TIN RIVER
KAM TIN ROAD
LAY DOWN AREA
CIVIL/BUILDING E&M
OHL BUILDING
PLANT ROOM
SIGNALING B.
PERMANENT W.
LAY DOWN AREA
D.G.S.
DIESEL S.
826800 E
826400 E
833600 N
833200 N
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATIONS
METRES
1 : 3000
ID NO
MONITORING LOCATION
AM4
DD110 LOT 482, WANG TOI SHAN
AM5
LEUNG UK TSUEN SQUATS

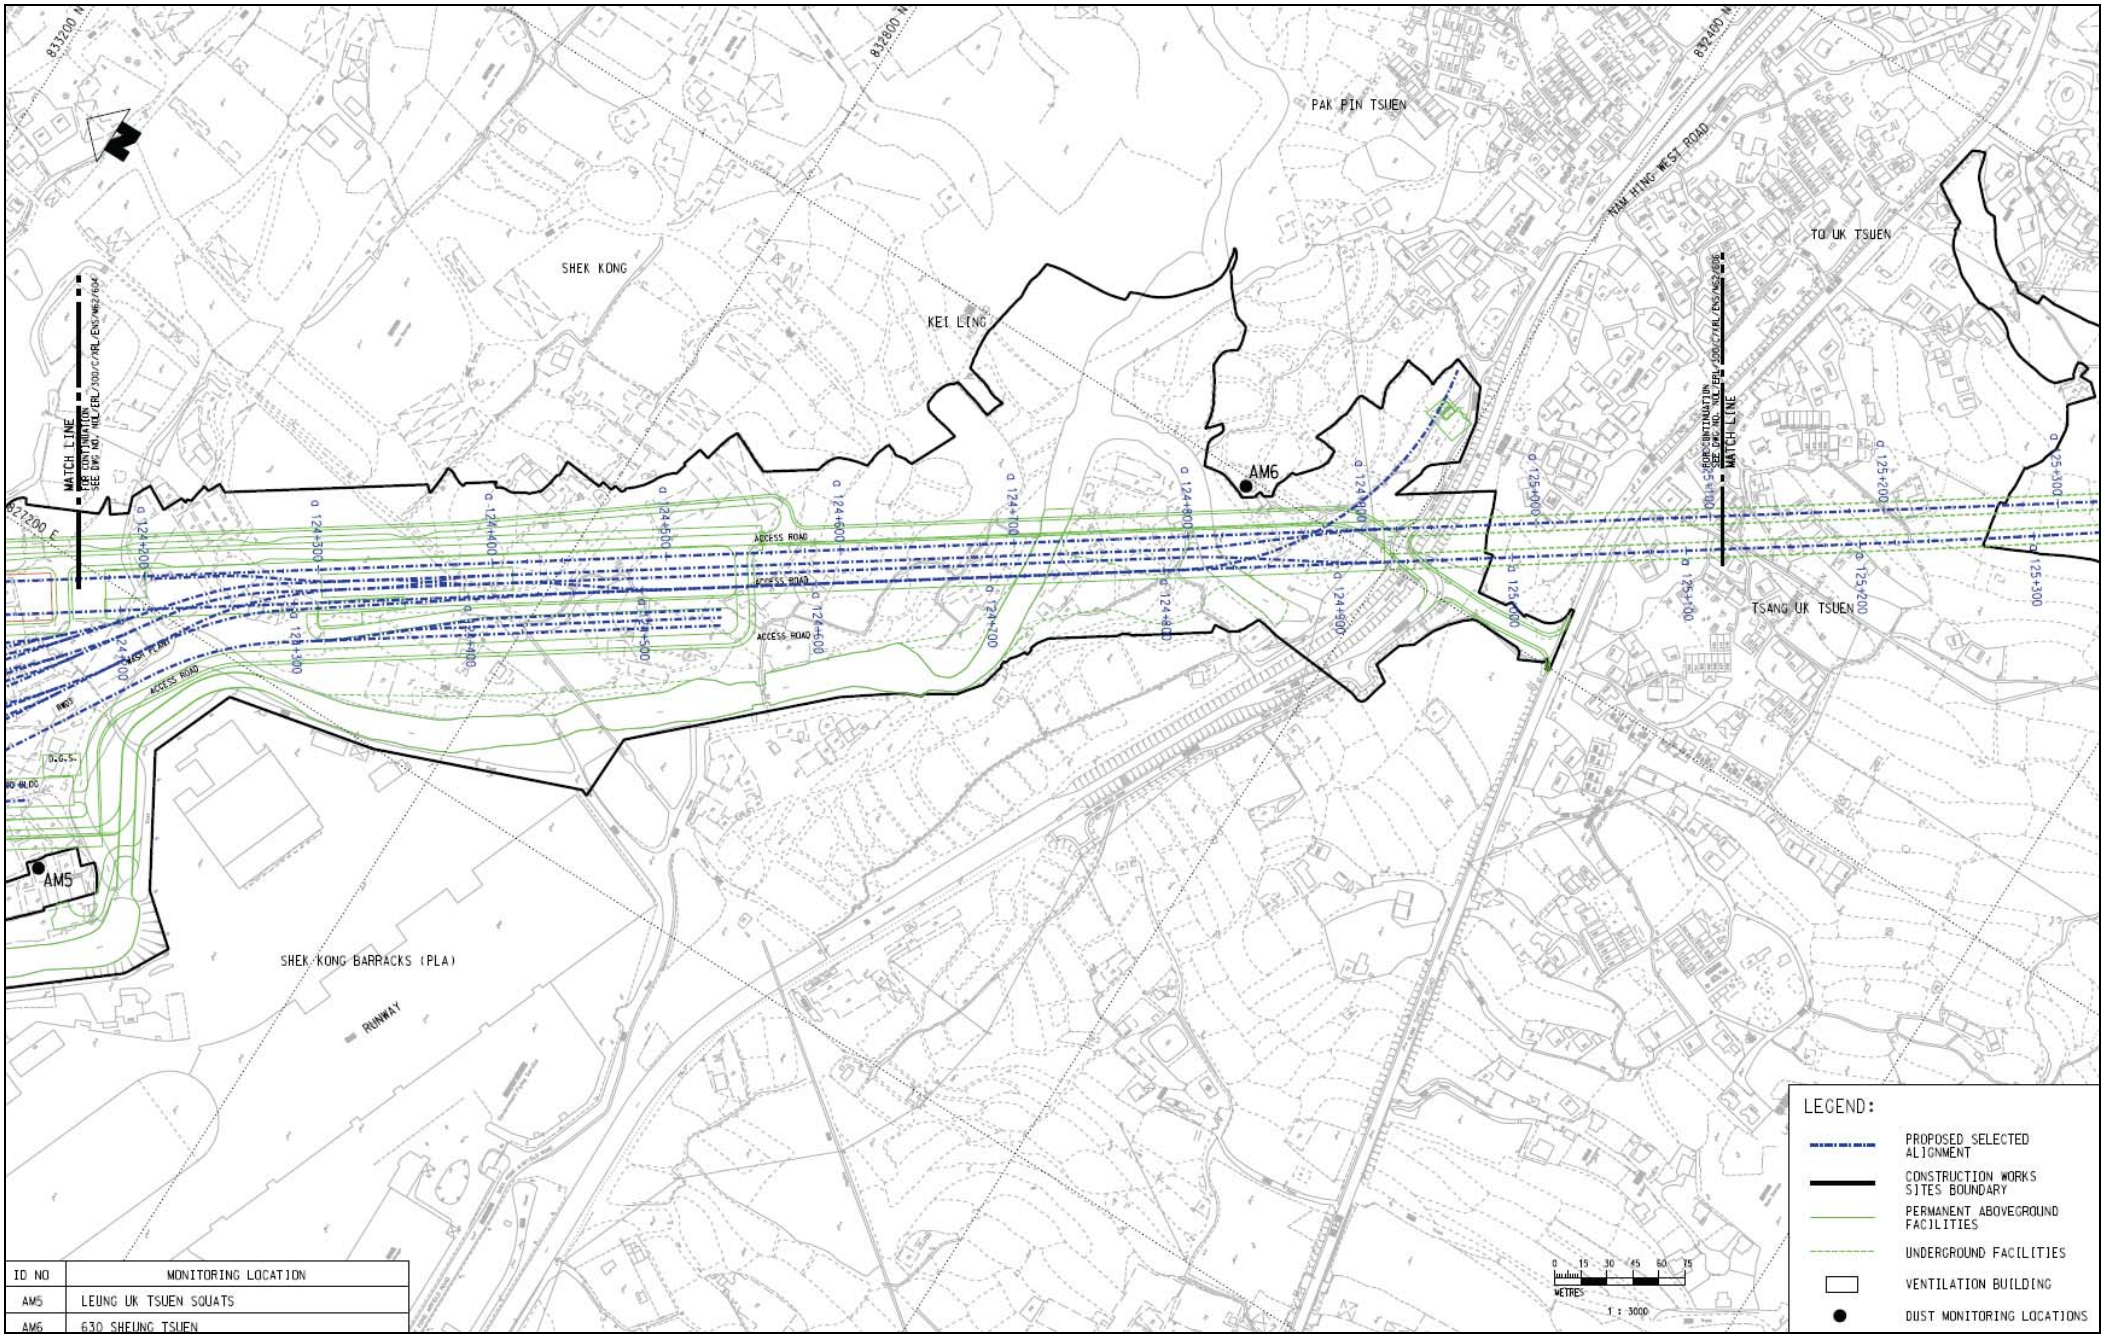



ID NO	MONITORING LOCATION
AM5	LEUNG UK TSUEN SQUATS
AM6	630 SHEUNG TSUEN

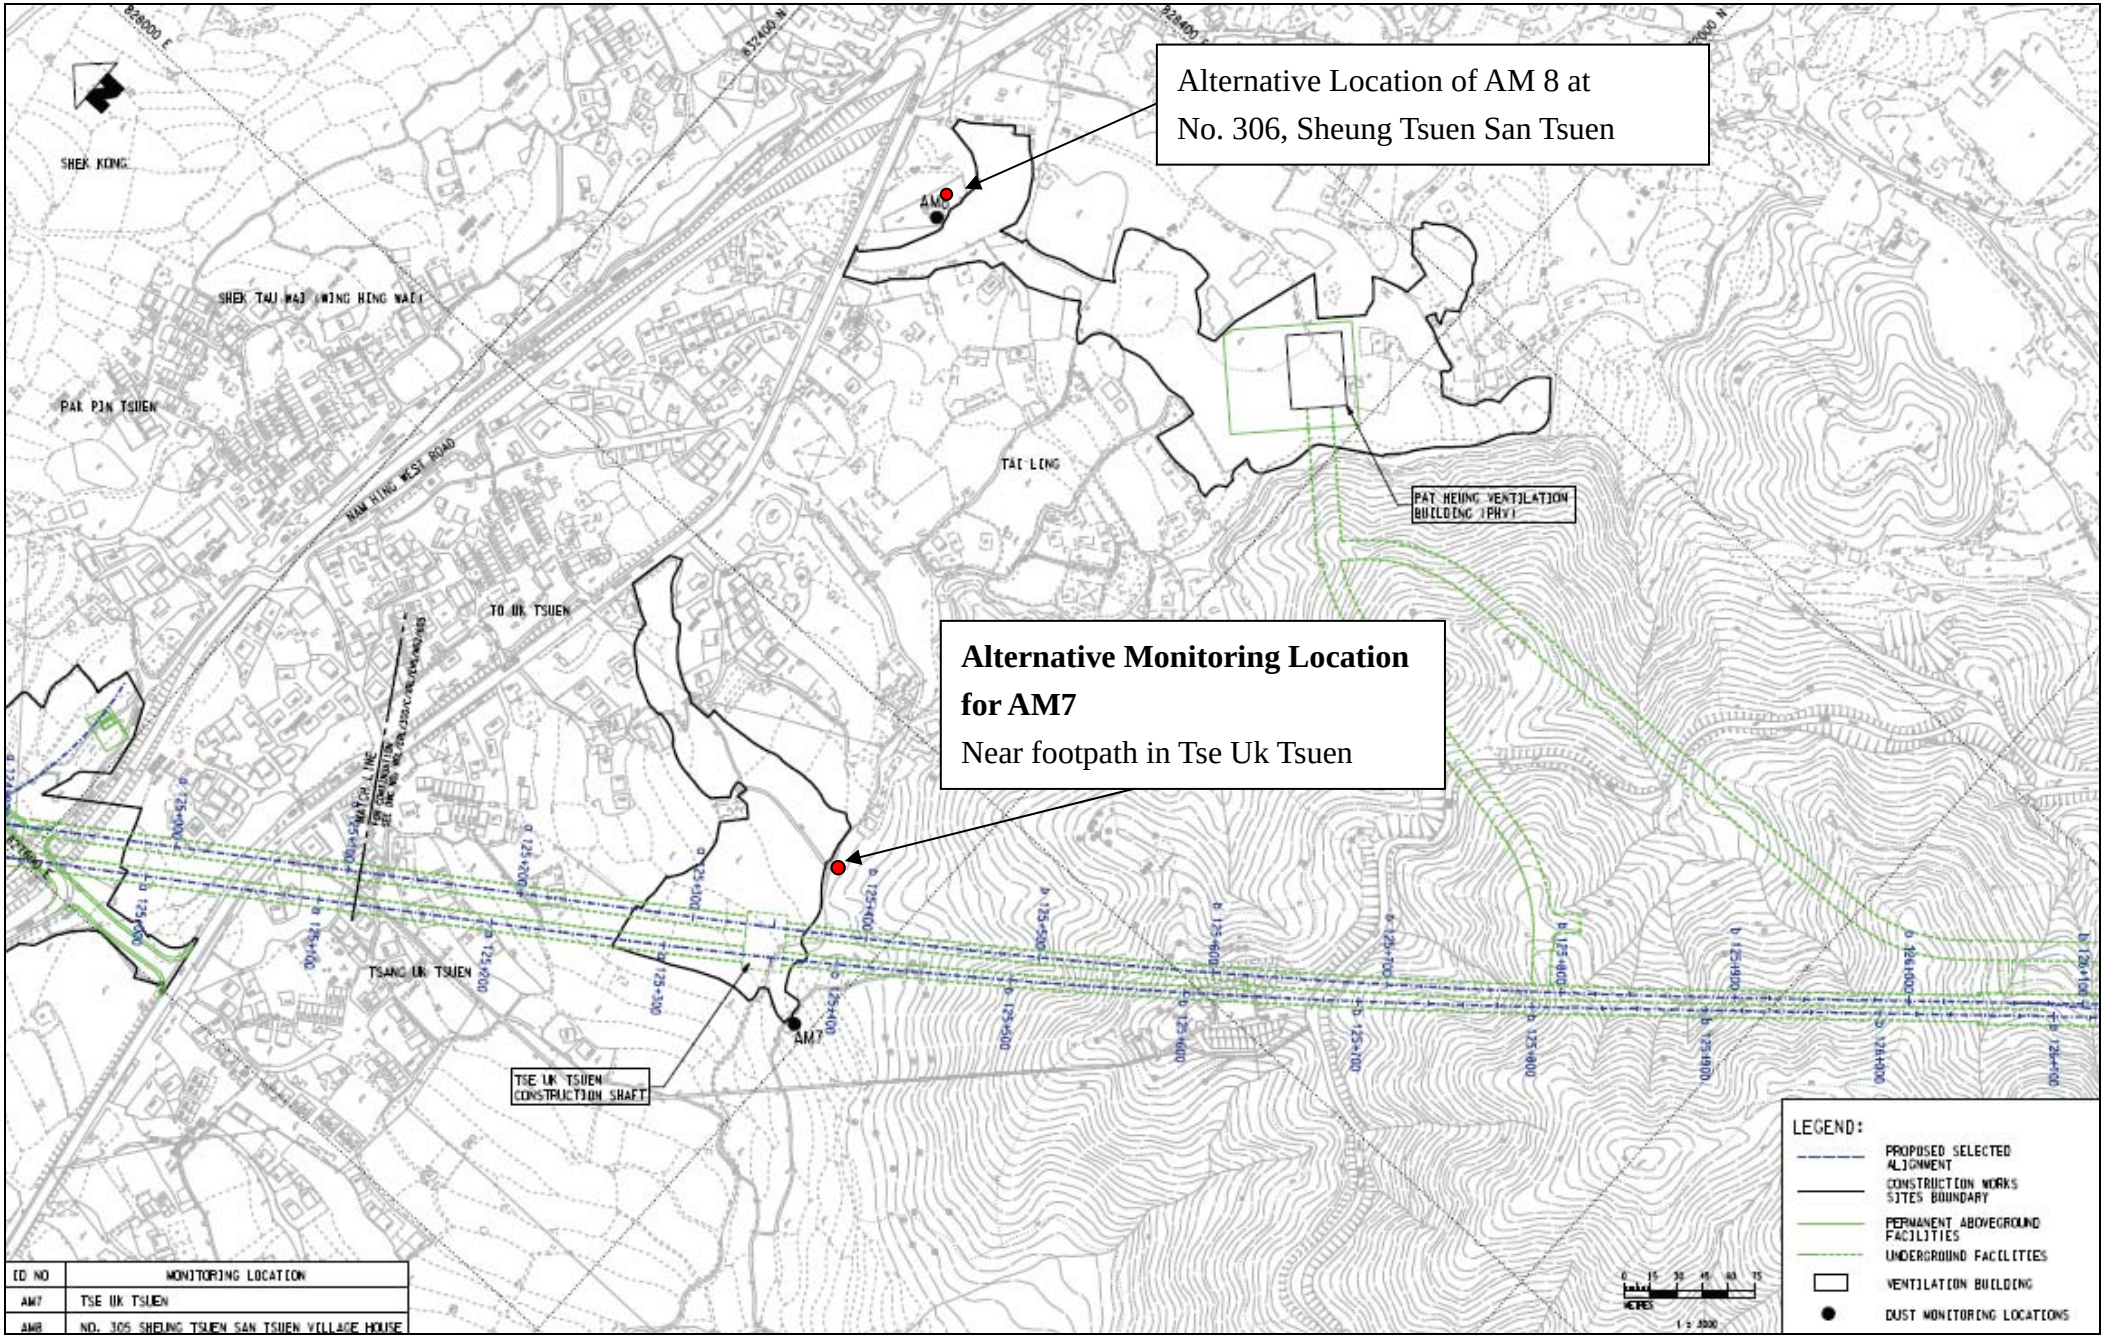
Alternative Location of AM 8 at
No. 306, Sheung Tsuen San Tsuen
Alternative Monitoring Location for AM7
Near footpath in Tse Uk Tsuen
AM8
AM7
SHEK KONG
SHEK TAU WAI (WING HING WAI)
PAK PIN TSUEN
WANG HING WEST ROAD
TAI LONG
PAT HEUNG VENTILATION BUILDING (PHV)
TO UK TSUEN
TSANG UK TSUEN
TSE UK TSUEN CONSTRUCTION SHAFT
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATIONS
ID NO
MONITORING LOCATION
AM7
TSE UK TSUEN
AM8
NO. 305 SHEUNG TSUEN SAN TSUEN VILLAGE HOUSE

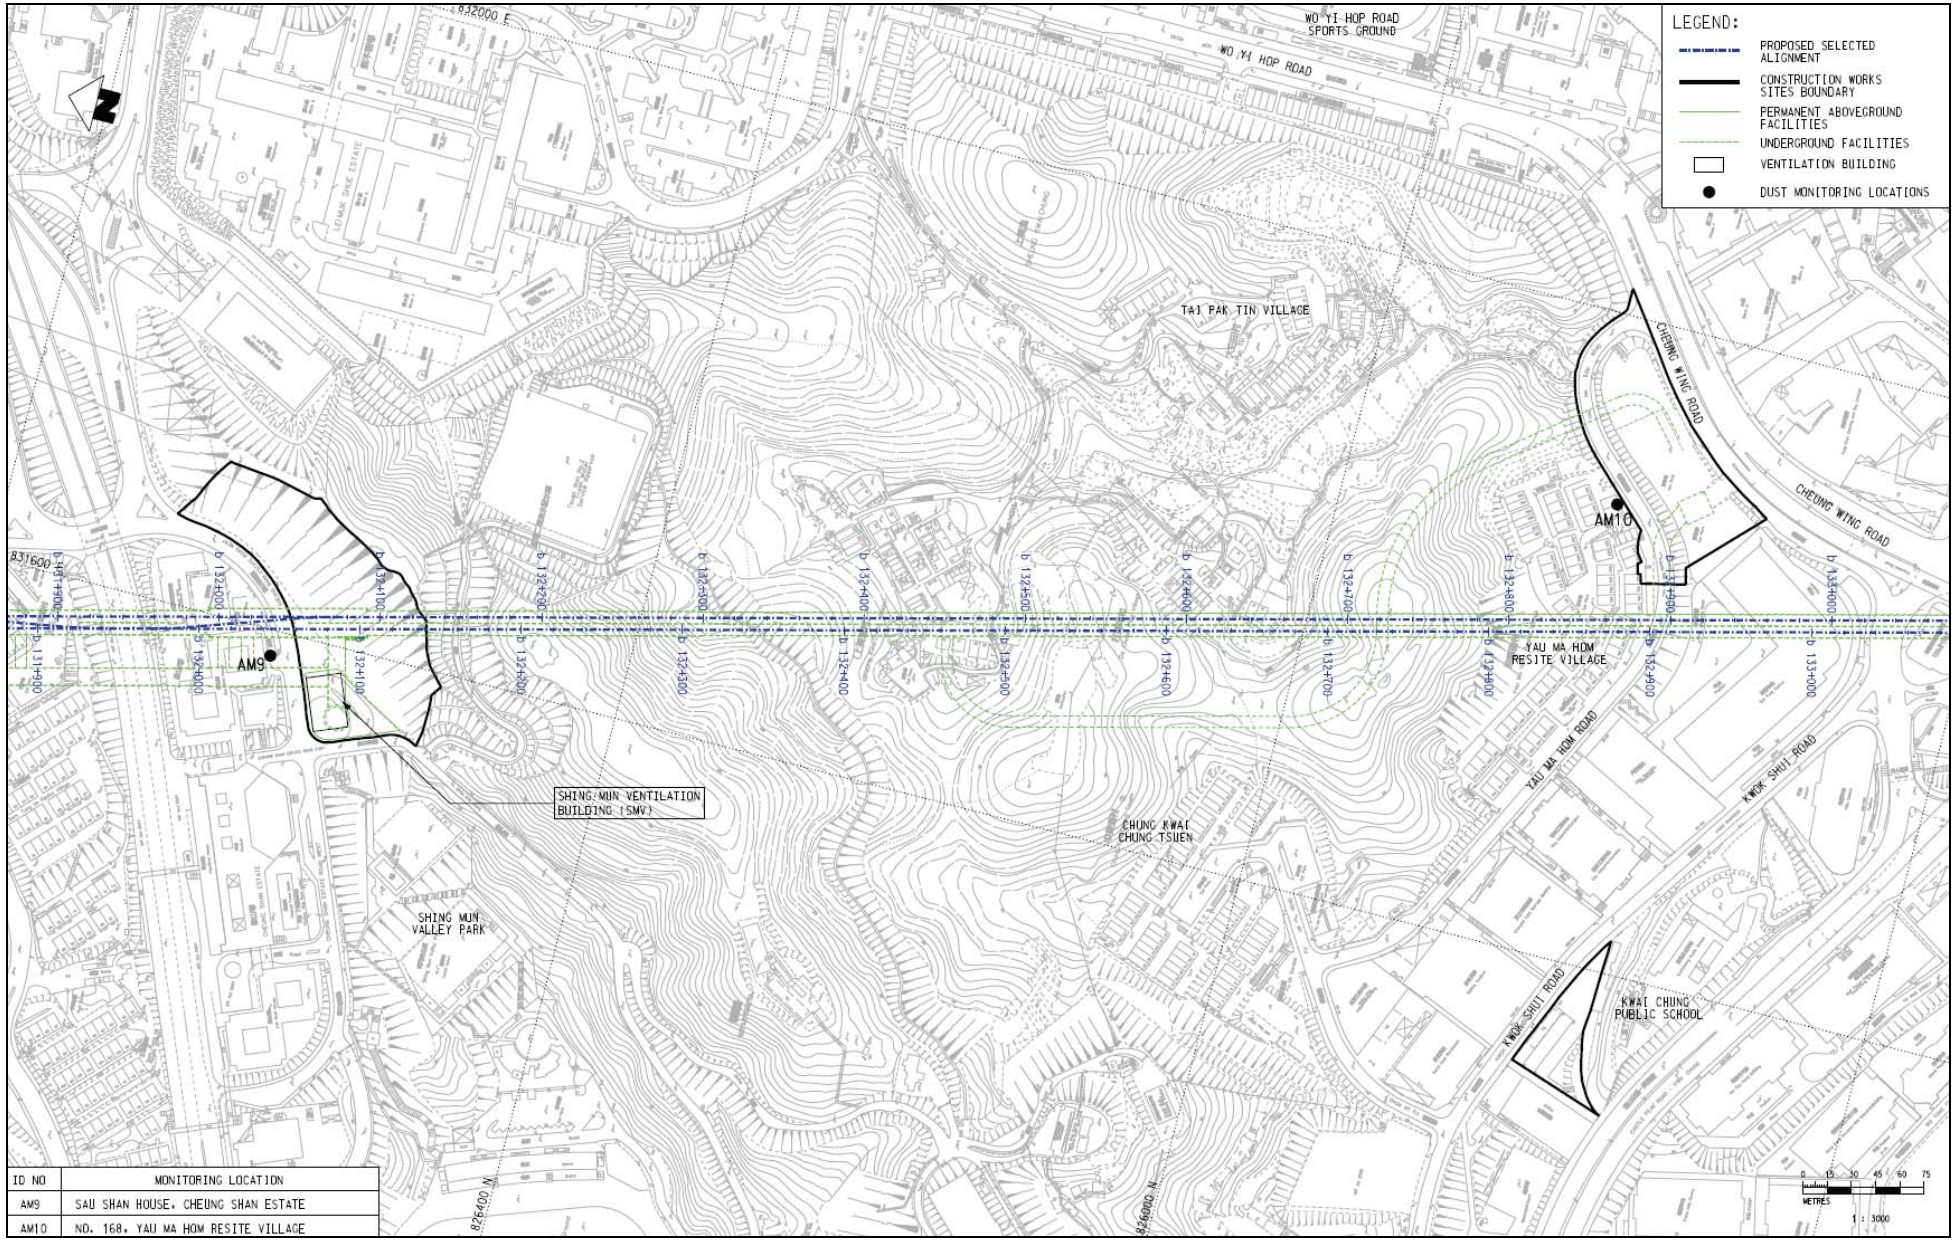


ID NO	MONITORING LOCATION
AM9	SAU SHAN HOUSE, CHEUNG SHAN ESTATE
AM10	NO. 168, YAU MA HOM RESITE VILLAGE

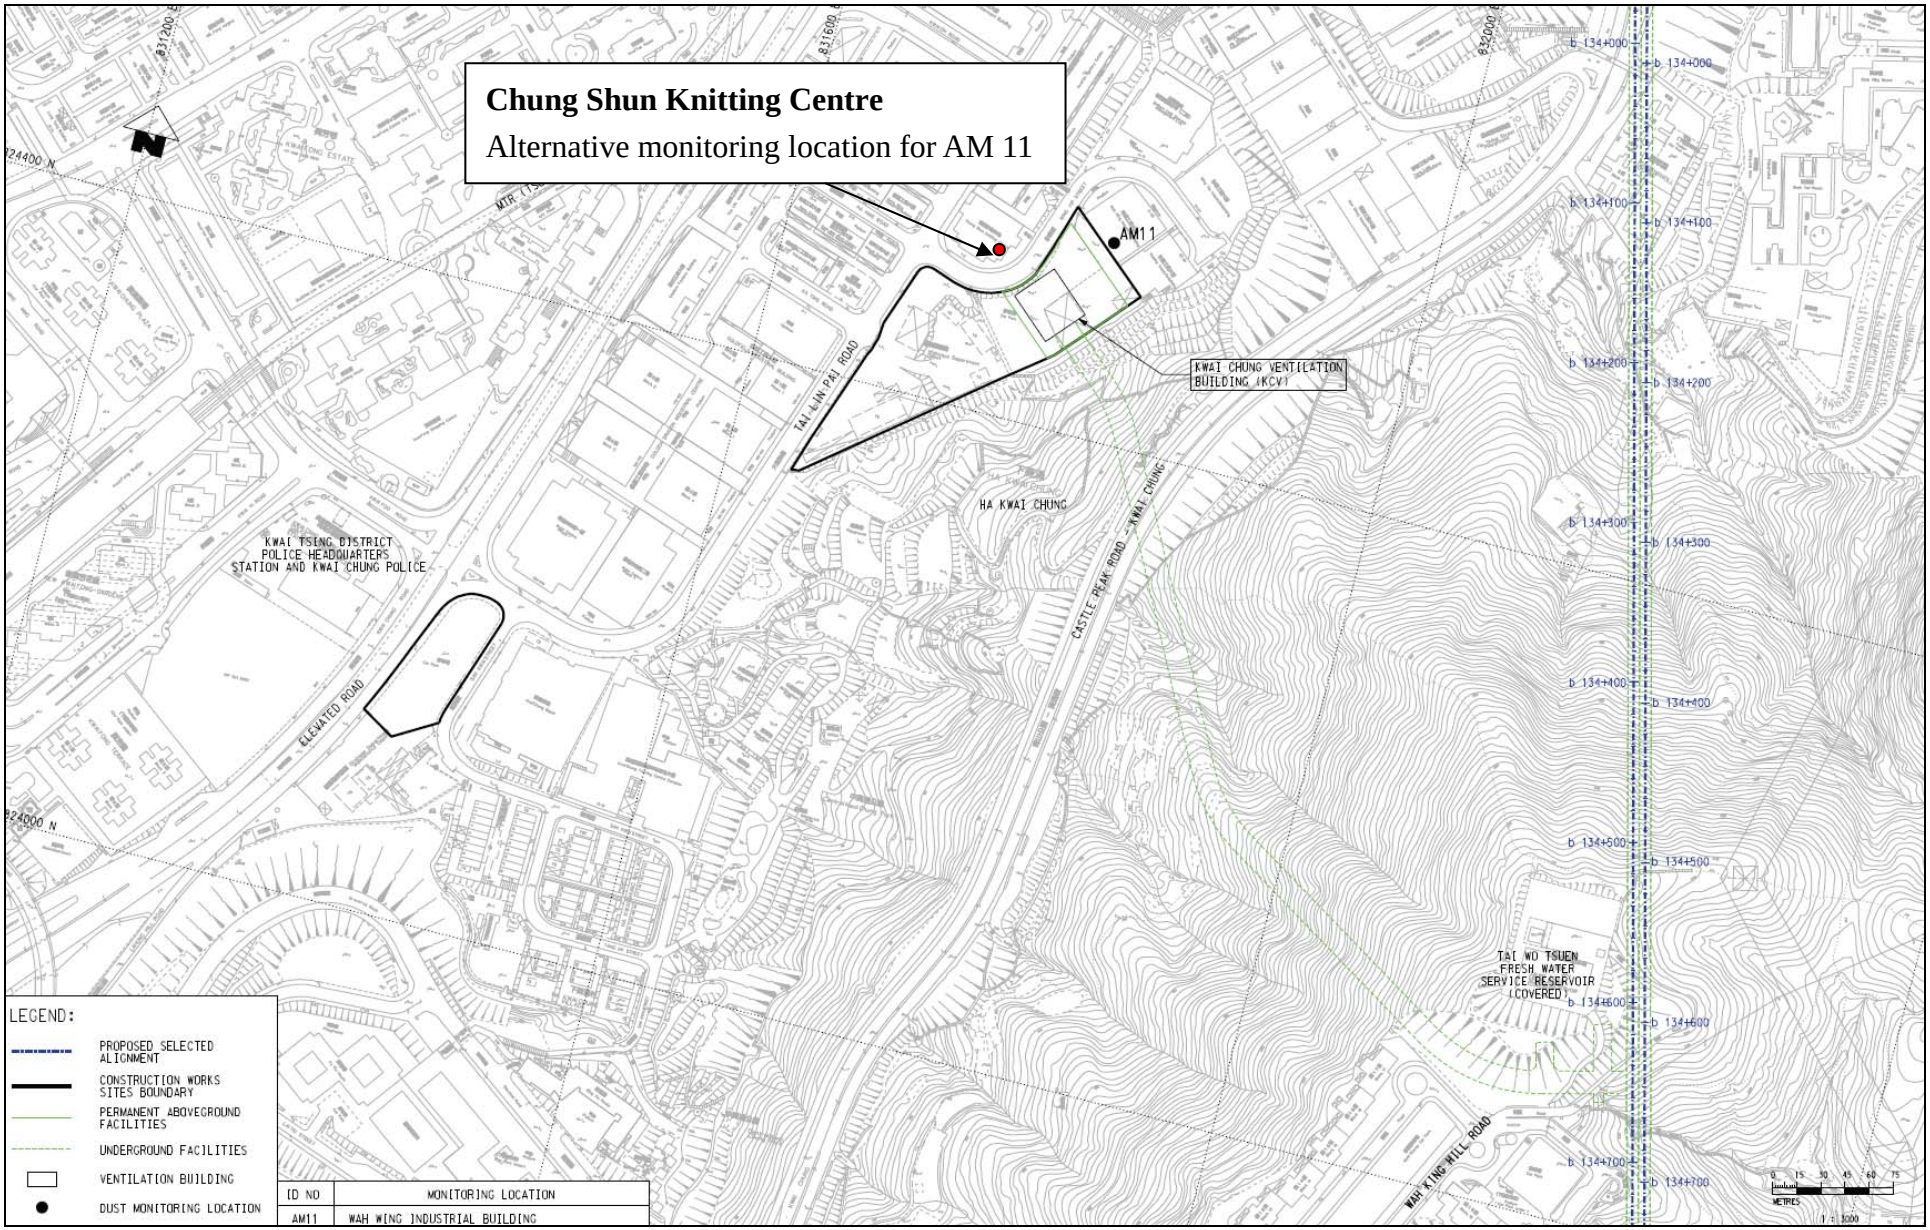

Chung Shun Knitting Centre
Alternative monitoring location for AM 11
AM11
KWAI CHUNG VENTILATION BUILDING (KCV)
TAI KLIN PAI ROAD
HA KWAI CHUNG
CASTLE PEAK ROAD - KWAI CHUNG
KWAI TSING DISTRICT POLICE HEADQUARTERS STATION AND KWAI CHUNG POLICE
ELEVATED ROAD
TAI WO TSUEN FRESH WATER SERVICE RESERVOIR (COVERED)
WAH KING HILL ROAD
LEGEND:
PROPOSED SELECTED ALIGNMENT
CONSTRUCTION WORKS SITES BOUNDARY
PERMANENT ABOVEGROUND FACILITIES
UNDERGROUND FACILITIES
VENTILATION BUILDING
DUST MONITORING LOCATION
ID NO
MONITORING LOCATION
AM11
WAH WING INDUSTRIAL BUILDING

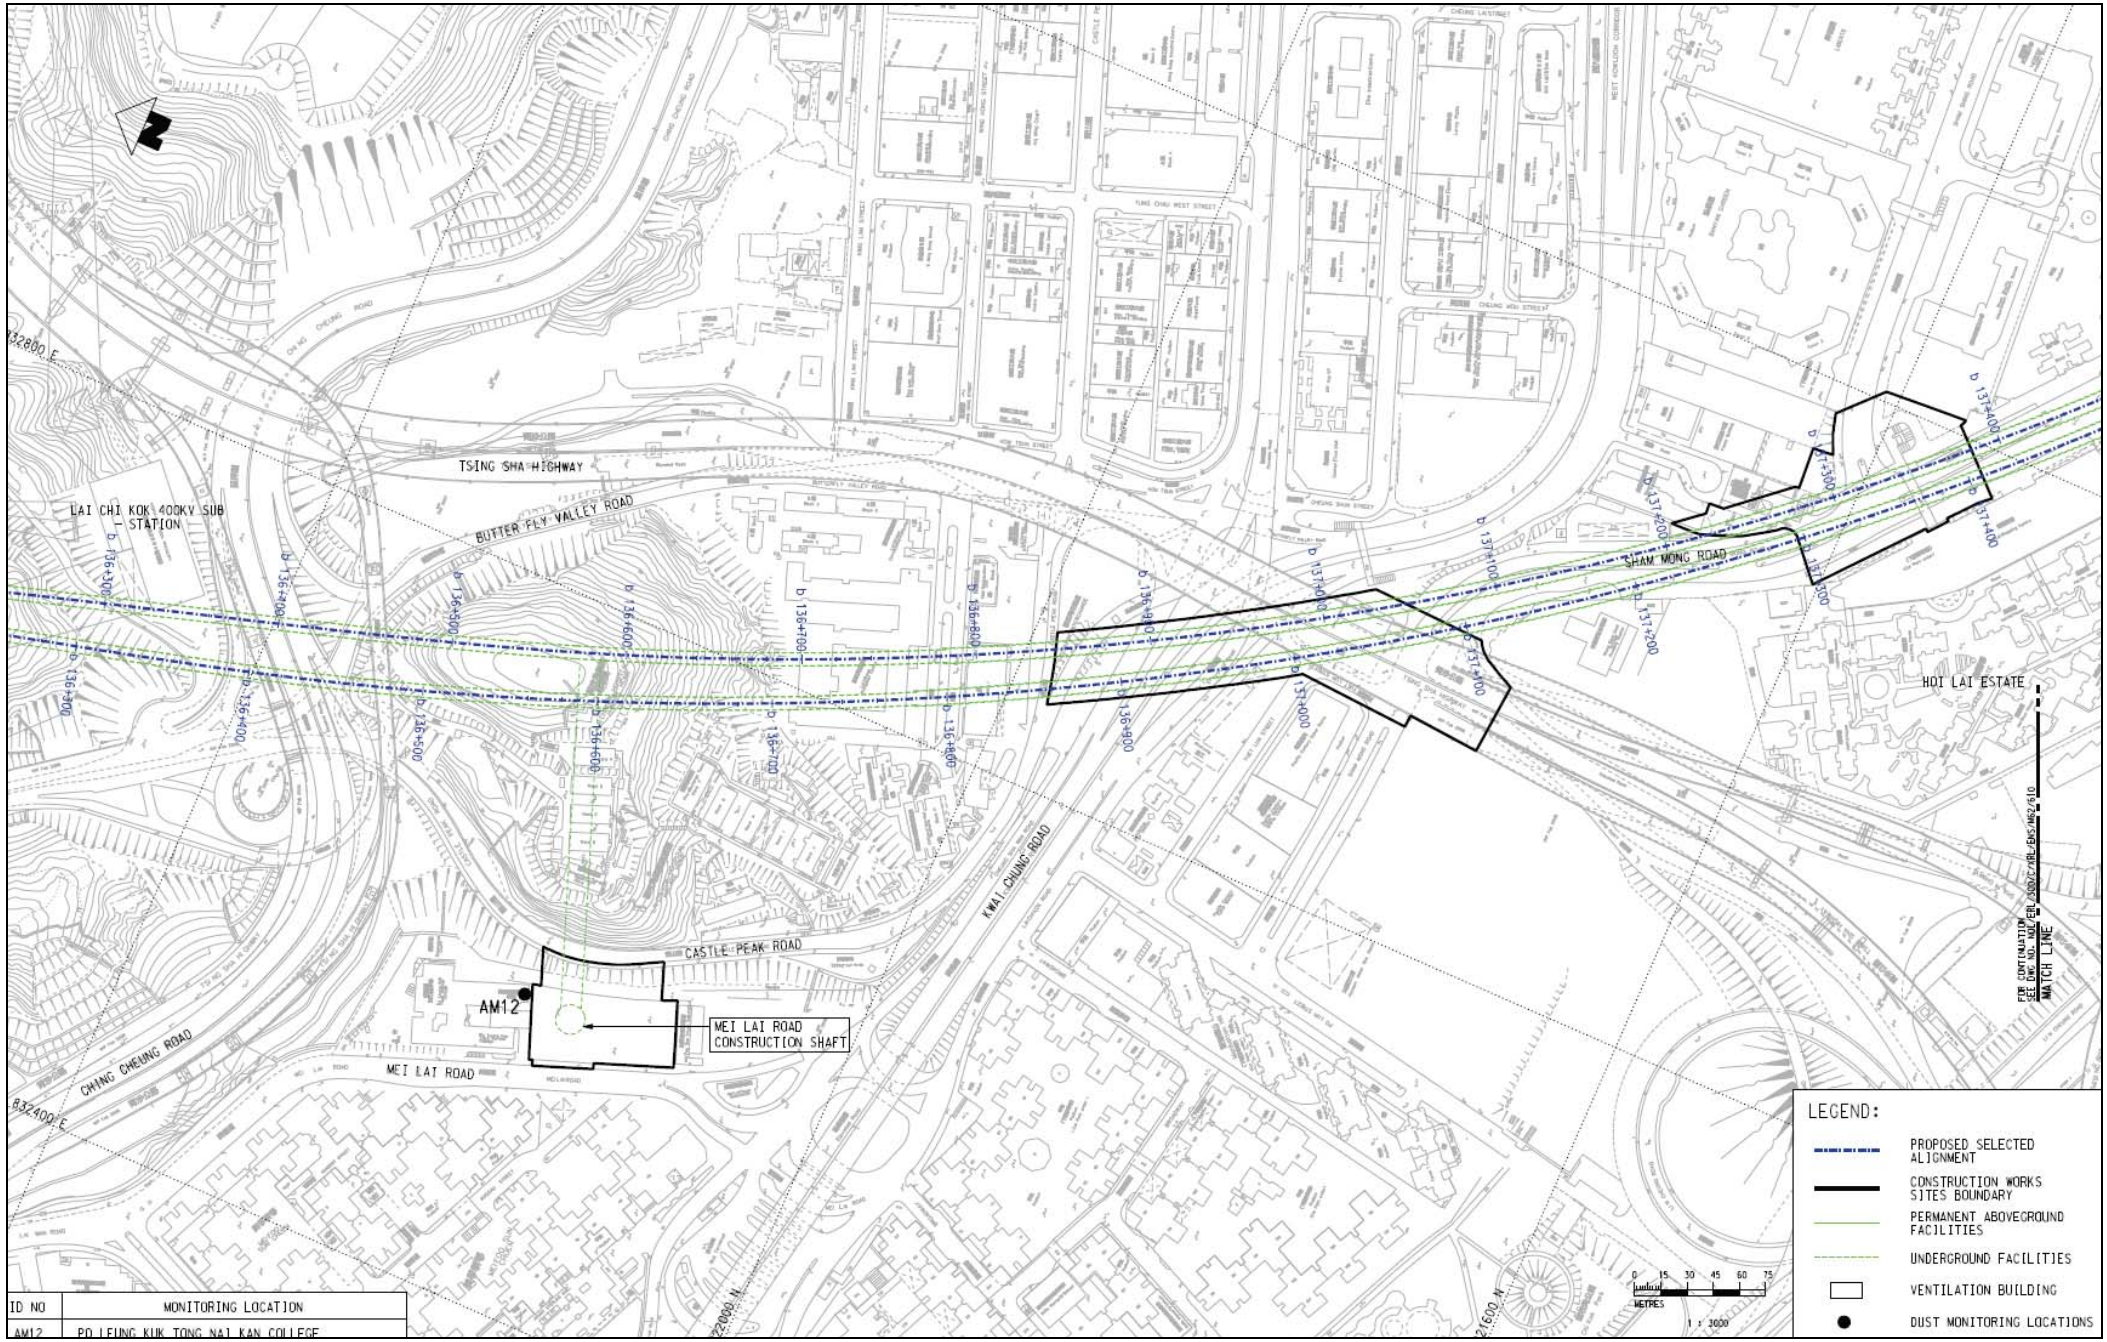


ID NO	MONITORING LOCATION
AM12	PO LEUNG KUK TONG NAI KAN COLLEGE

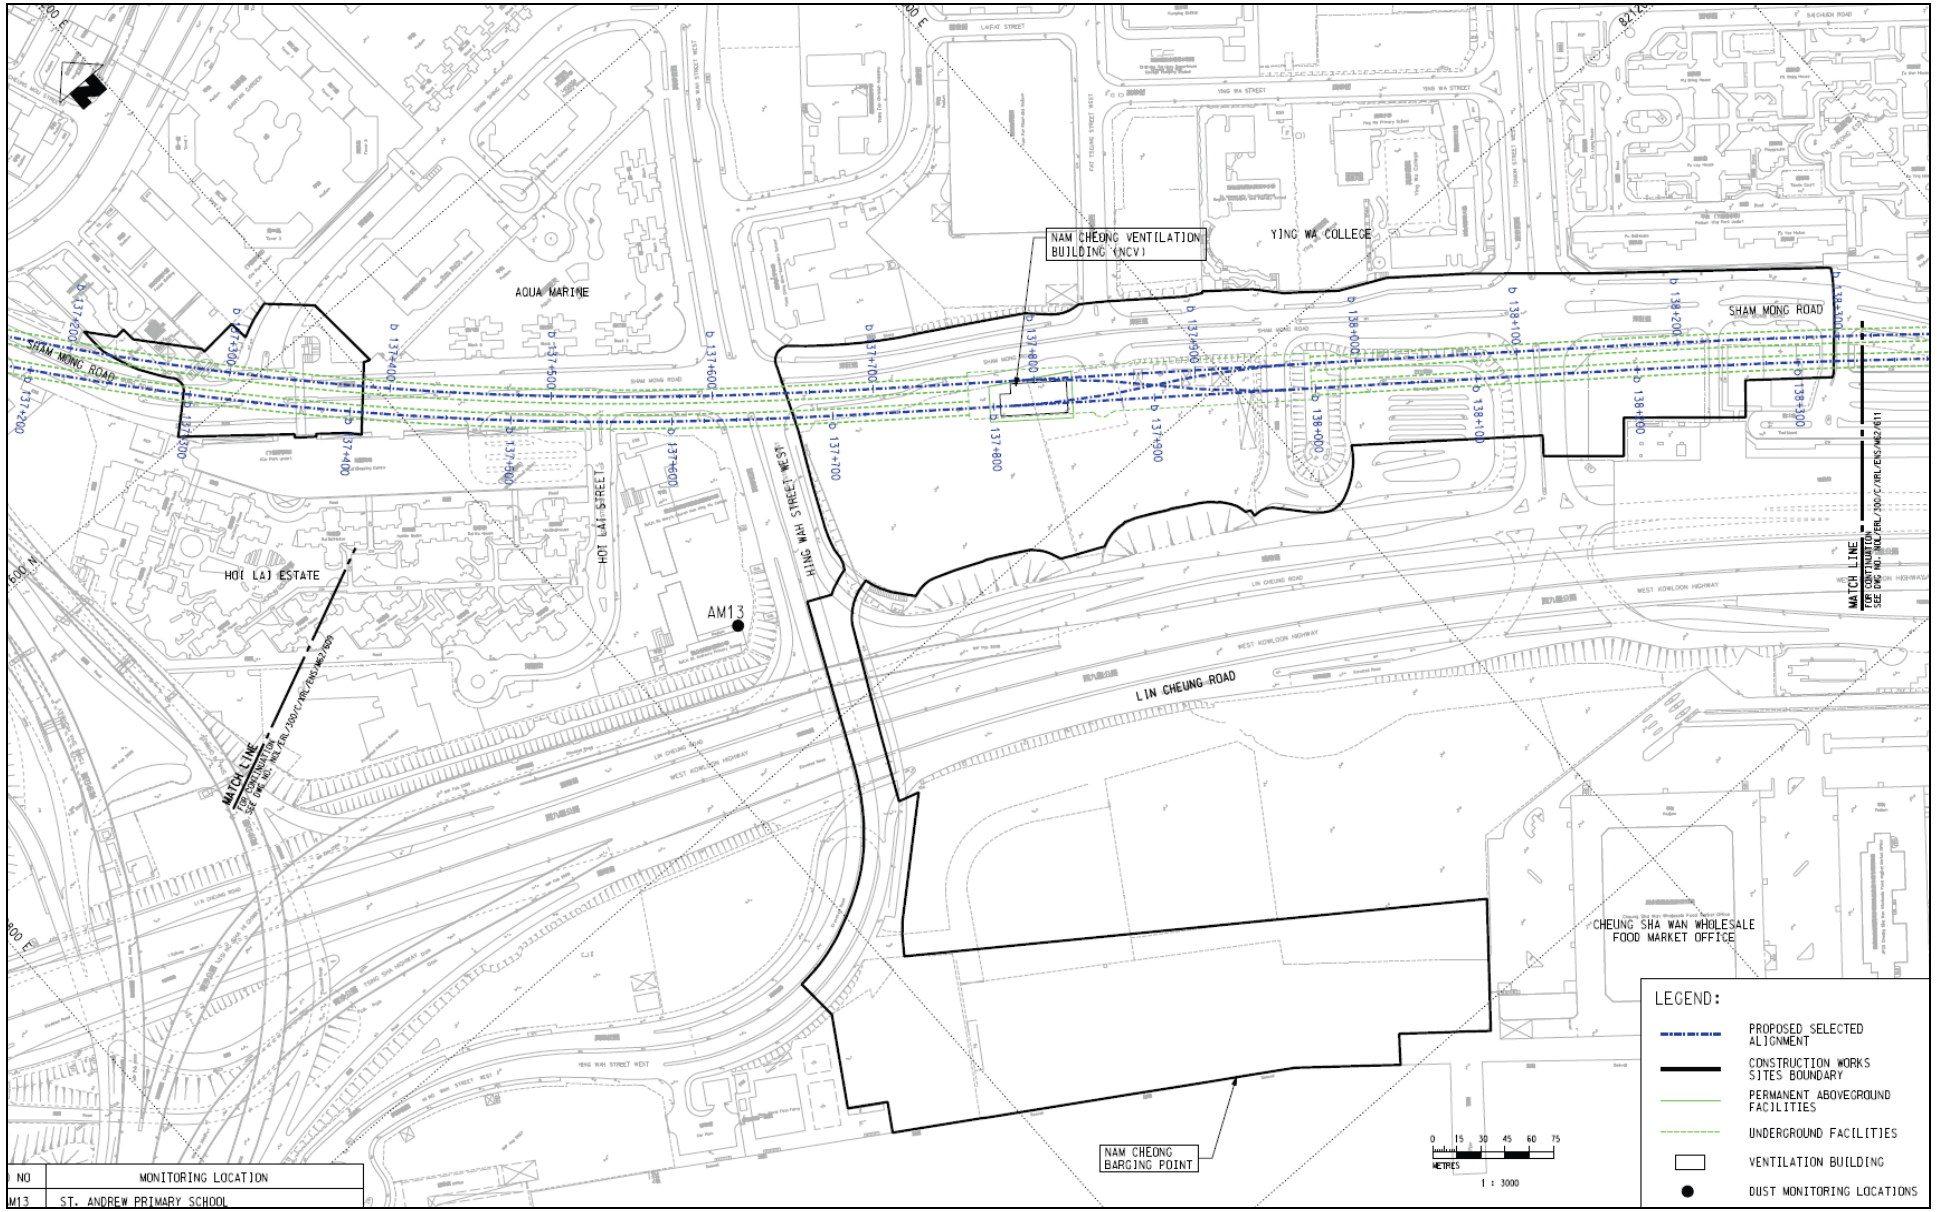


NO	MONITORING LOCATION
M13	ST. ANDREW PRIMARY SCHOOL

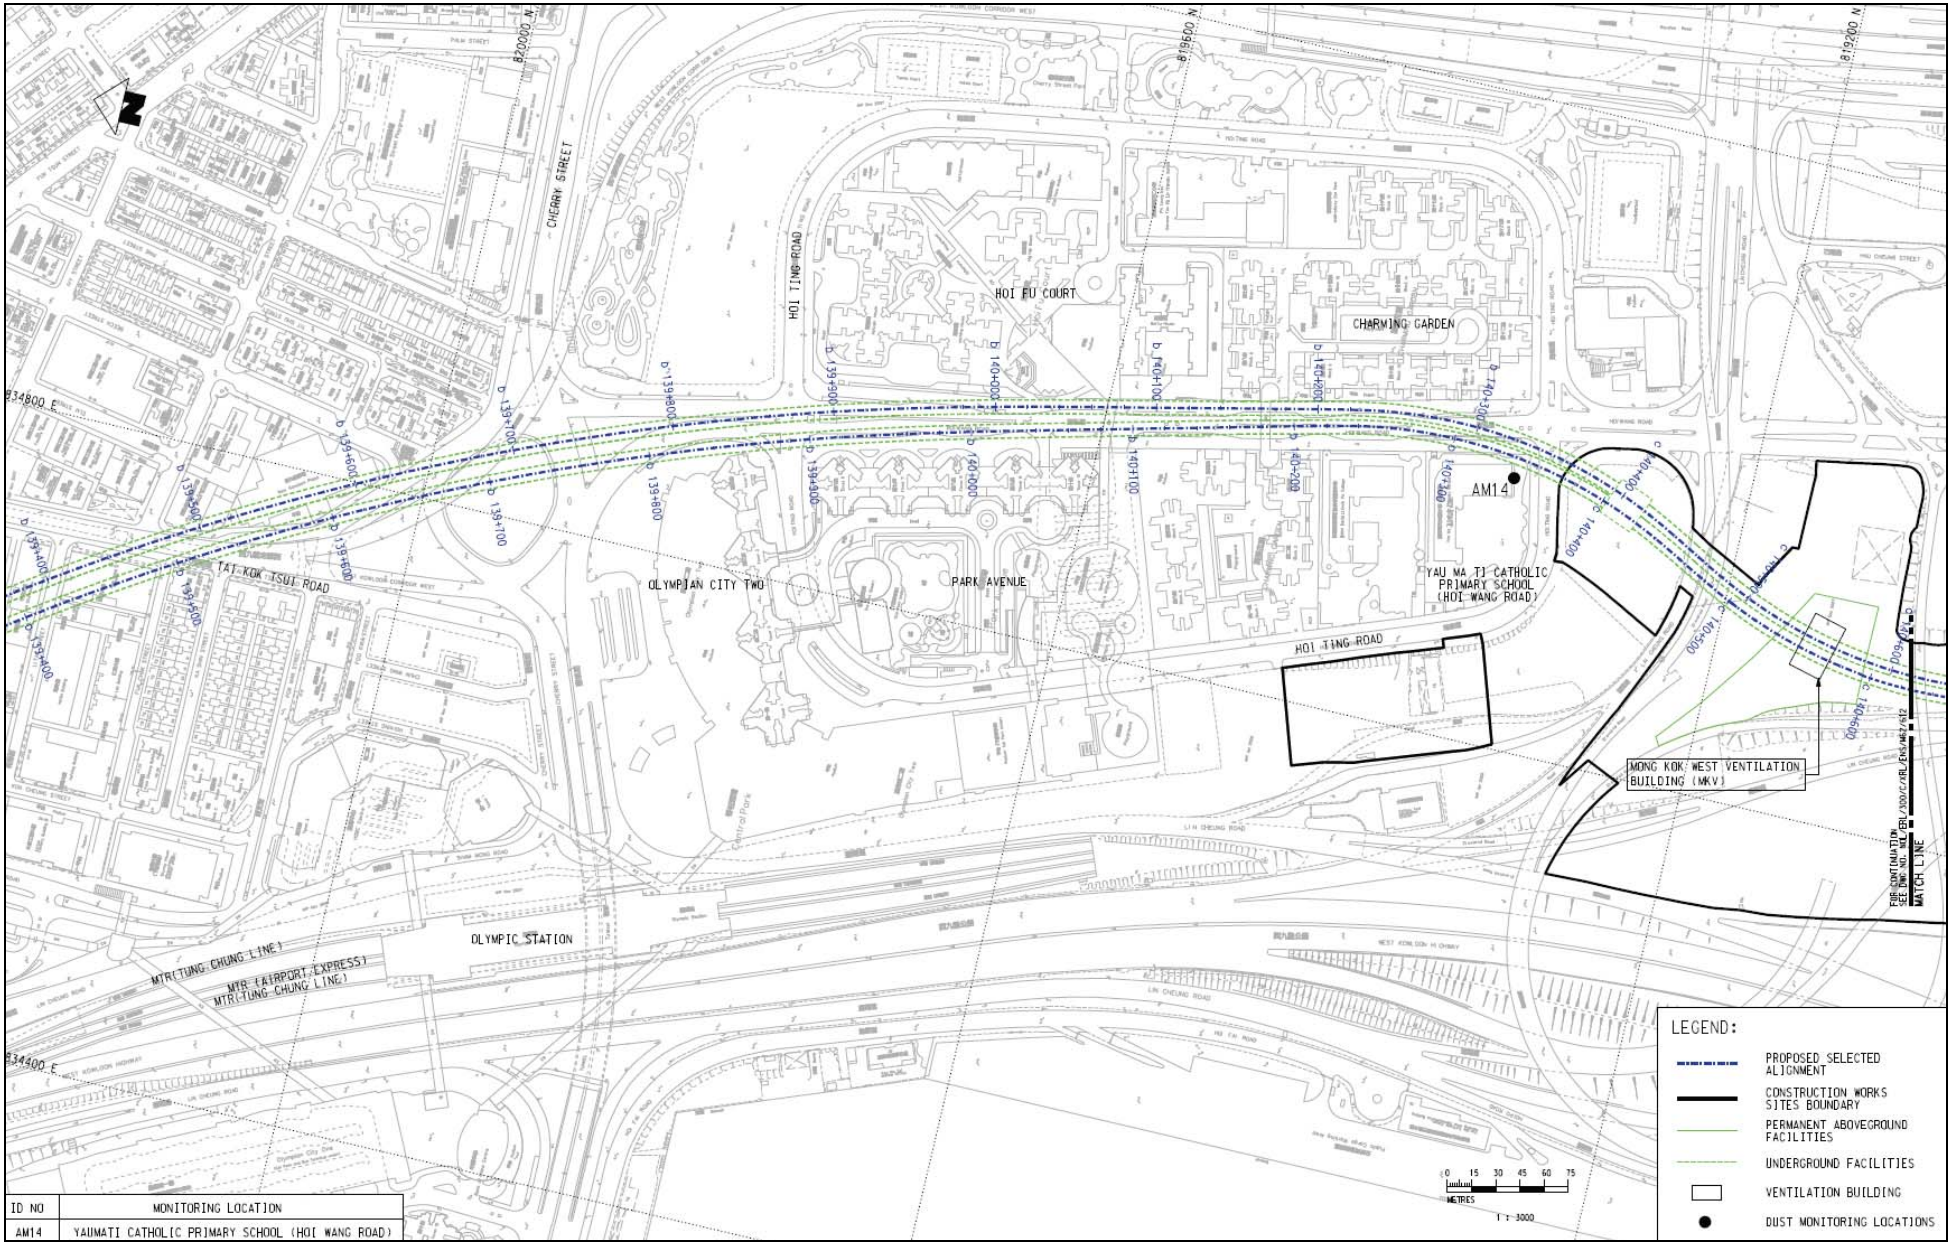

ID NO	MONITORING LOCATION
AM14	YAUMATI CATHOLIC PRIMARY SCHOOL (HOI WANG ROAD)

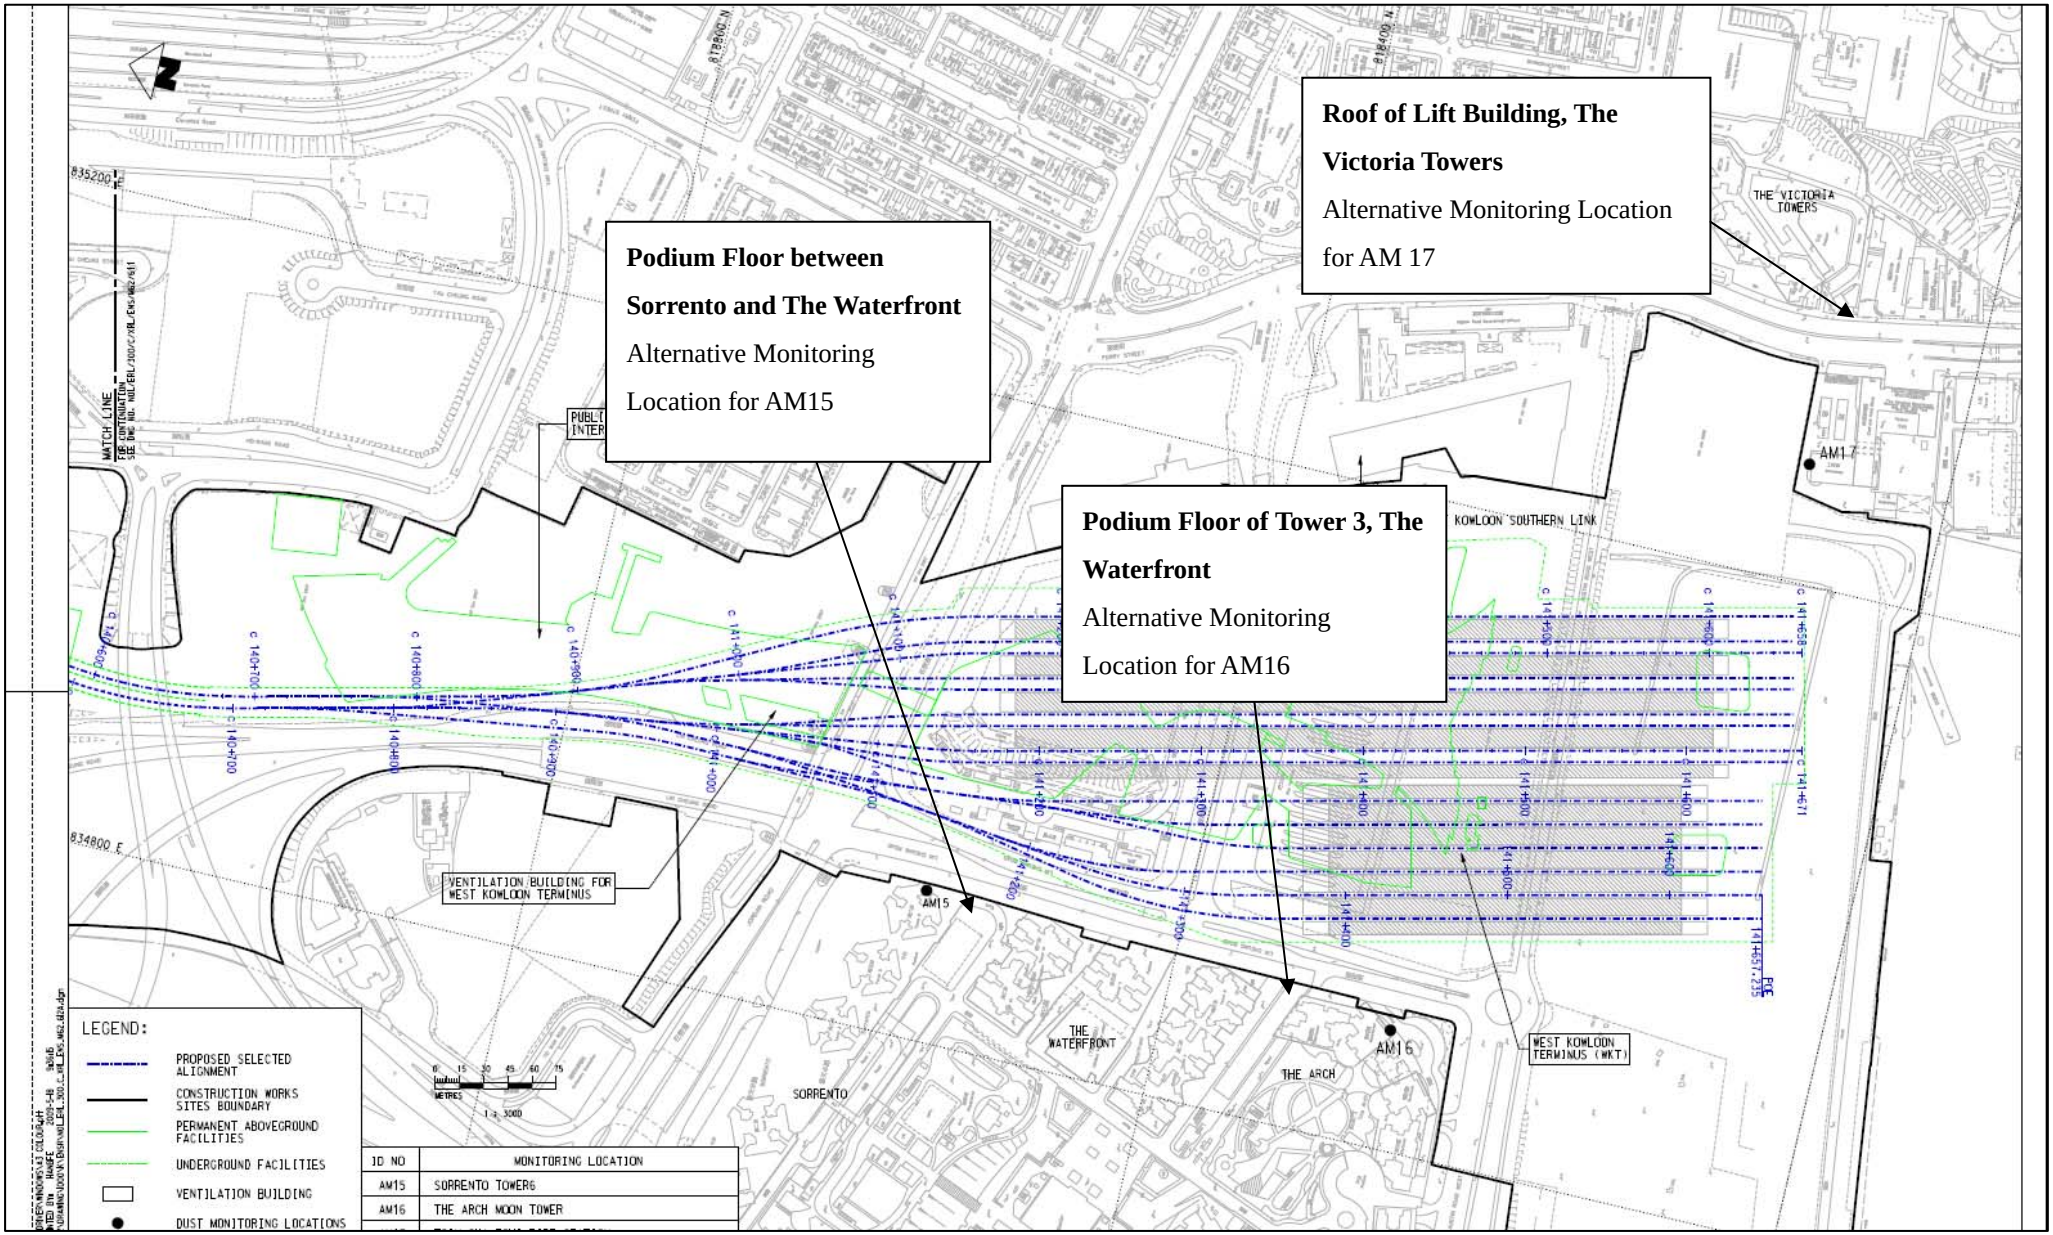

Dust monitoring locations

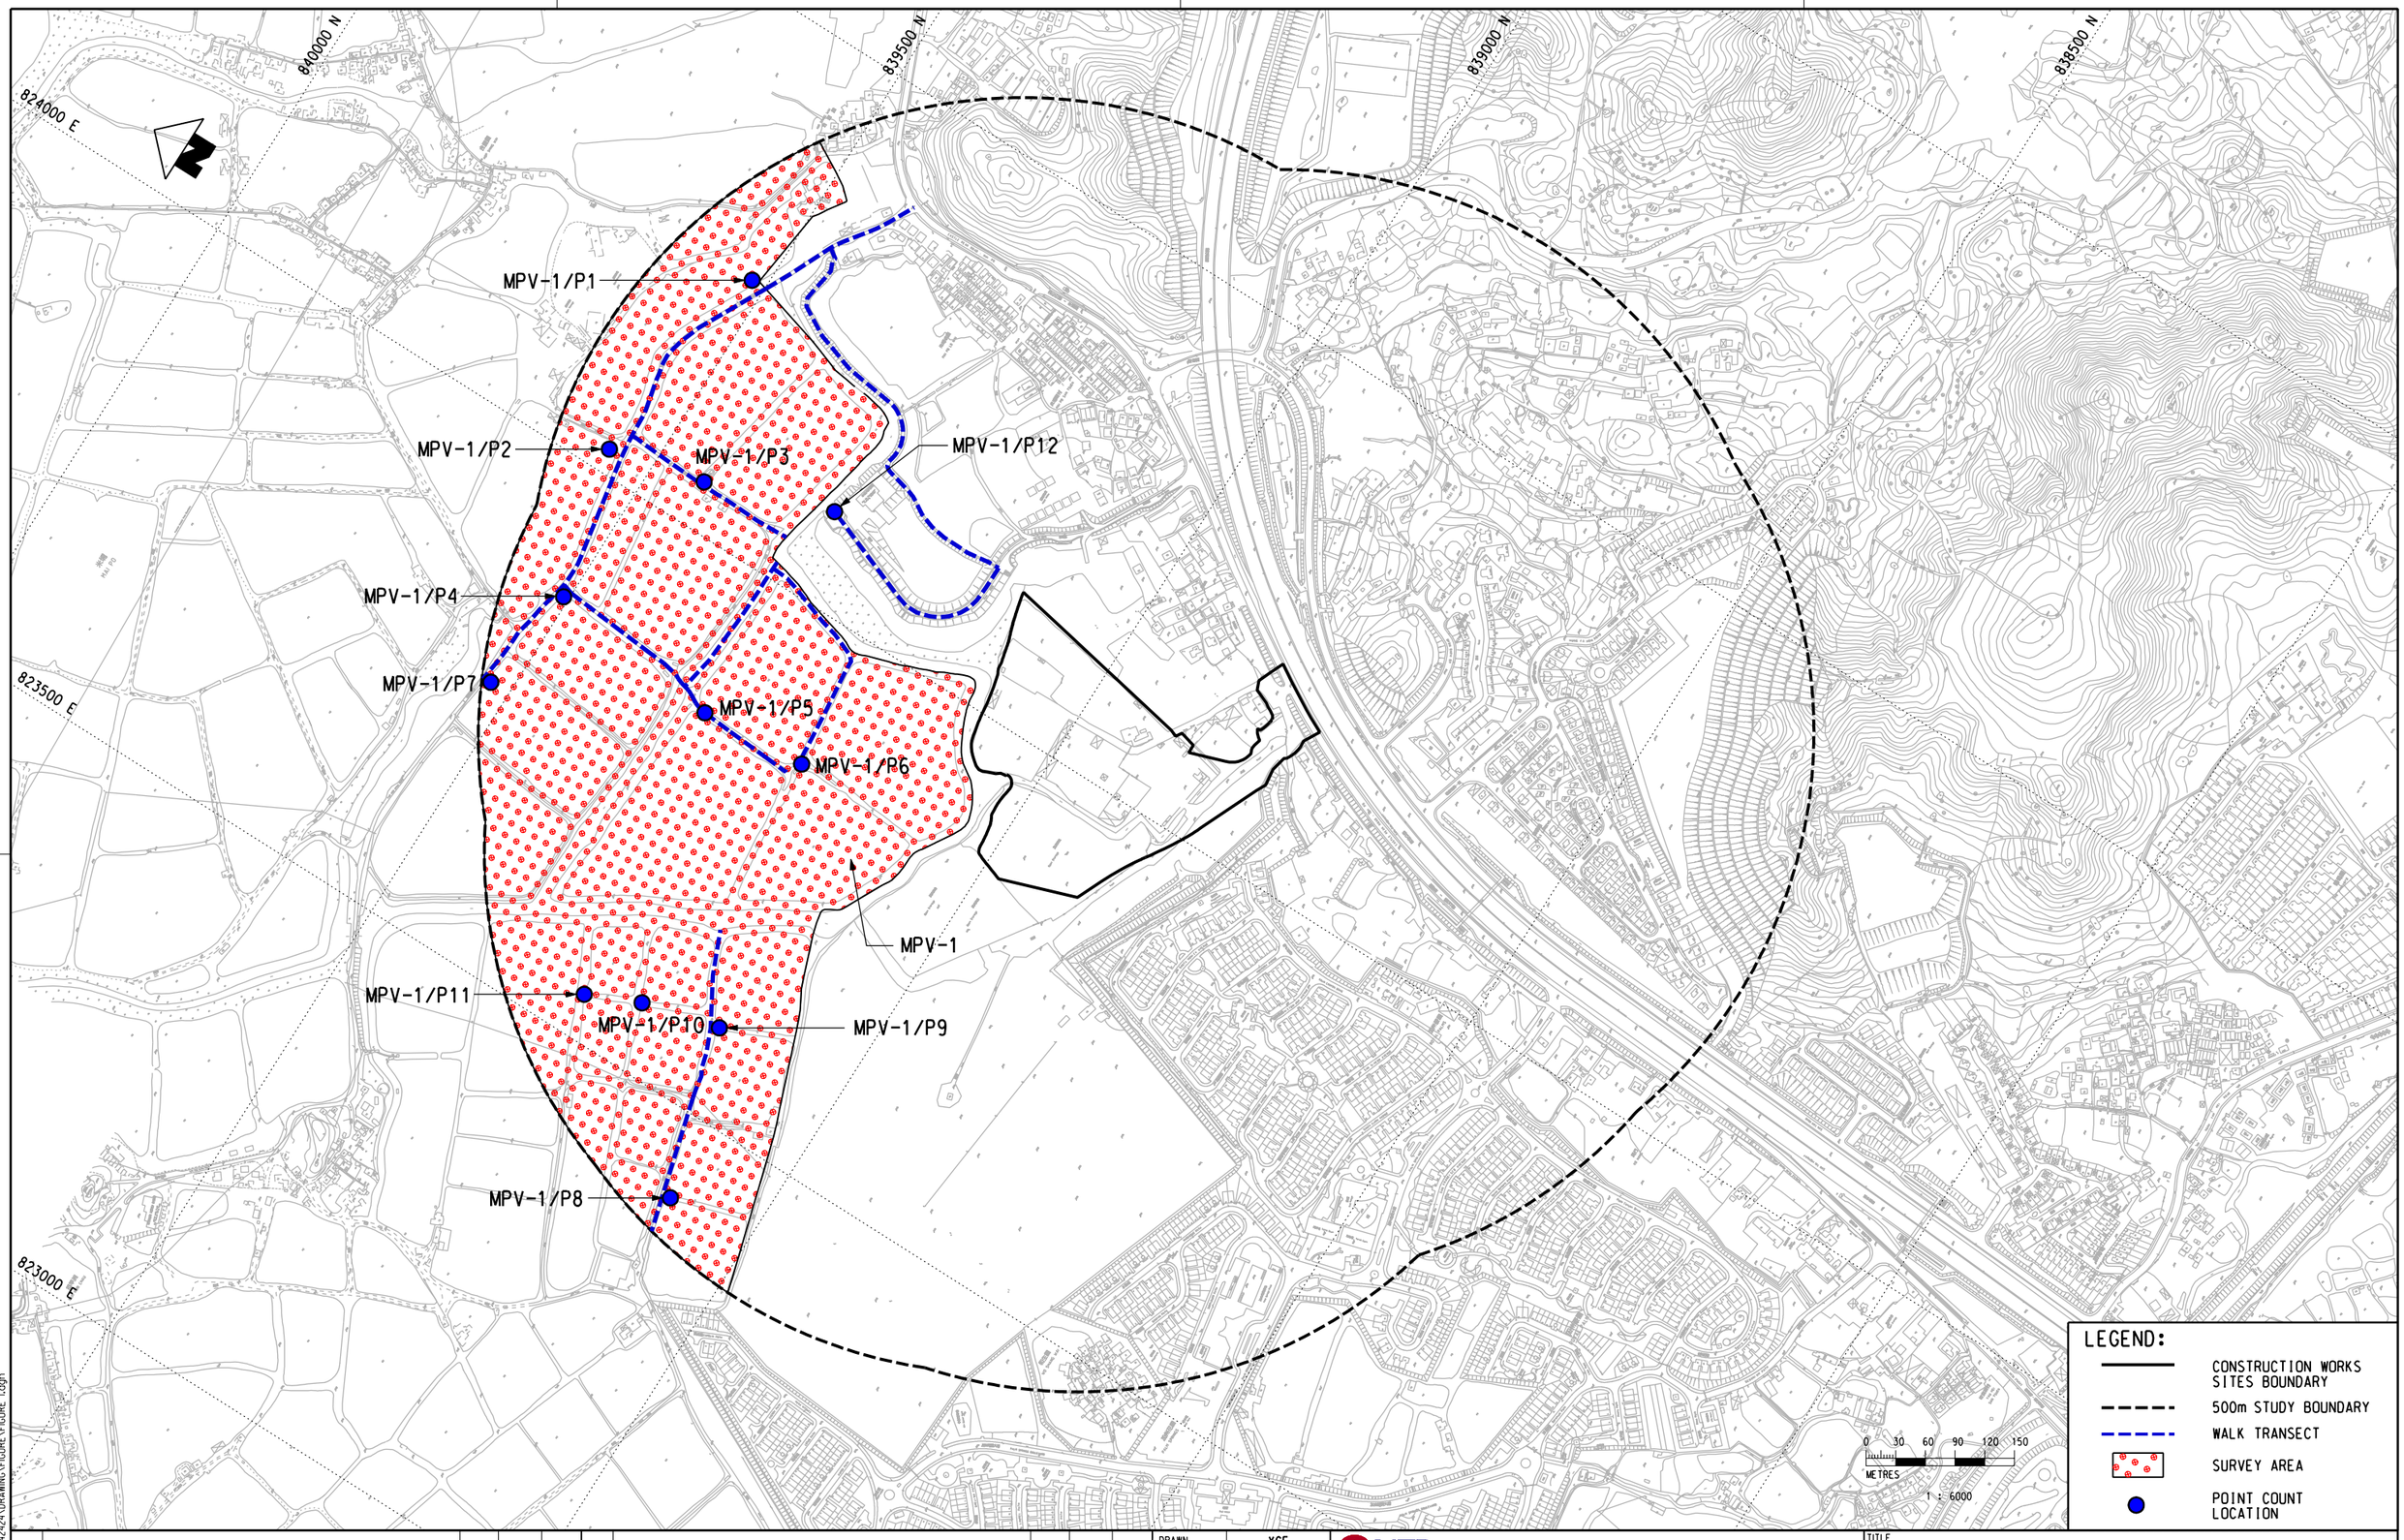

REV	DESCRIPTION	BY	DATE	APPROVED

REV	DESCRIPTION	BY	DATE	APPROVED

DRAWN	XCF
DESIGNED	TWF
CHECKED	KCC
APPROVED	PL
DATE	10/OCT./2008

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
© MTR CORPORATION LIMITED 2008 COPYRIGHT IN RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY THE MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE DRAWING / DOCUMENT OR ANY PART BY WHATEVER MEANS IS PERMITTED WITHOUT THE PRIOR WRITTEN CONSENT OF THE MTR CORPORATION LIMITED.

MTR

EXPRESS RAIL LINK

ORIGINATOR

AECOM

CADD REF.
FIGURE 1.dgn

TITLE
NOL / ERL-300
BASELINE BIRD SURVEY FOR EIA
PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR MPV-1

SCALE	FIGURE NO.	REV.
1 : 6000 (A3)	FIGURE 1	–

PLOT DRV: r:\ustrnset\MTR\PLOTDRVER\WINDOWS\A3 COLOUR.pH
MODELNAME: Default PRINTED BY: CHENYG 2010-2-5
FILENAME: p:\PROJECTS\60042424\DRAWINGS\FIGURE 1.dgn 859947

834500 N
834000 N
833500 N
824000 E
824500 E
825000 E
825500 E

43CD-1
TPP-3/P3
TPP-3/P1
TPP-3/P2
TPP-3
TPP-2/P4
95CD
TPP-2/P3
TPP-2
TPP-2/P2
TPP-2/P1

0 30 60 90 120 150
METRES
1 : 6000

LEGEND:
- CONSTRUCTION WORKS SITES BOUNDARY
- 500m STUDY BOUNDARY
- WALK TRANSECT
- SURVEY AREA
- POINT COUNT LOCATION

PLOT DRV
MODELNAME:
FILENAME: F:\lastmod\WATER\PLOTDRV\ERWINDOWS\AS COLOUR.plt
DEFAULT
DATA\PROJECTS\60412470\DRAWING\FIGURE\FIGURE 2.dgn
PRINTED BY: spmyg
2009-11 13:51:44

REV	DESCRIPTION	BY	DATE	APPROVED	REV	DESCRIPTION	BY	DATE	APPROVED


DRAWN	YJP
DESIGNED	TWF
CHECKED	KCC
APPROVED	PL
DATE	14/SEP./2009

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
© MTR CORPORATION (LOTS) 2008 COPYRIGHT IN RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY THE MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE DRAWING / DOCUMENT OR ANY PART BY WHATEVER MEANS IS PERMITTED WITHOUT THE PRIOR WRITTEN CONSENT OF THE MTR CORPORATION LIMITED.

MTR
EXPRESS RAIL LINK
ORIGINATOR
AECOM
CADD REF. FIGURE 2.dgn

TITLE
NOL / ERL-300
BASELINE BIRD SURVEY FOR EIA
PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR TPP-2 AND TPP-3

SCALE	FIGURE NO.	REV
1 : 6000 (A3)	FIGURE 2	-

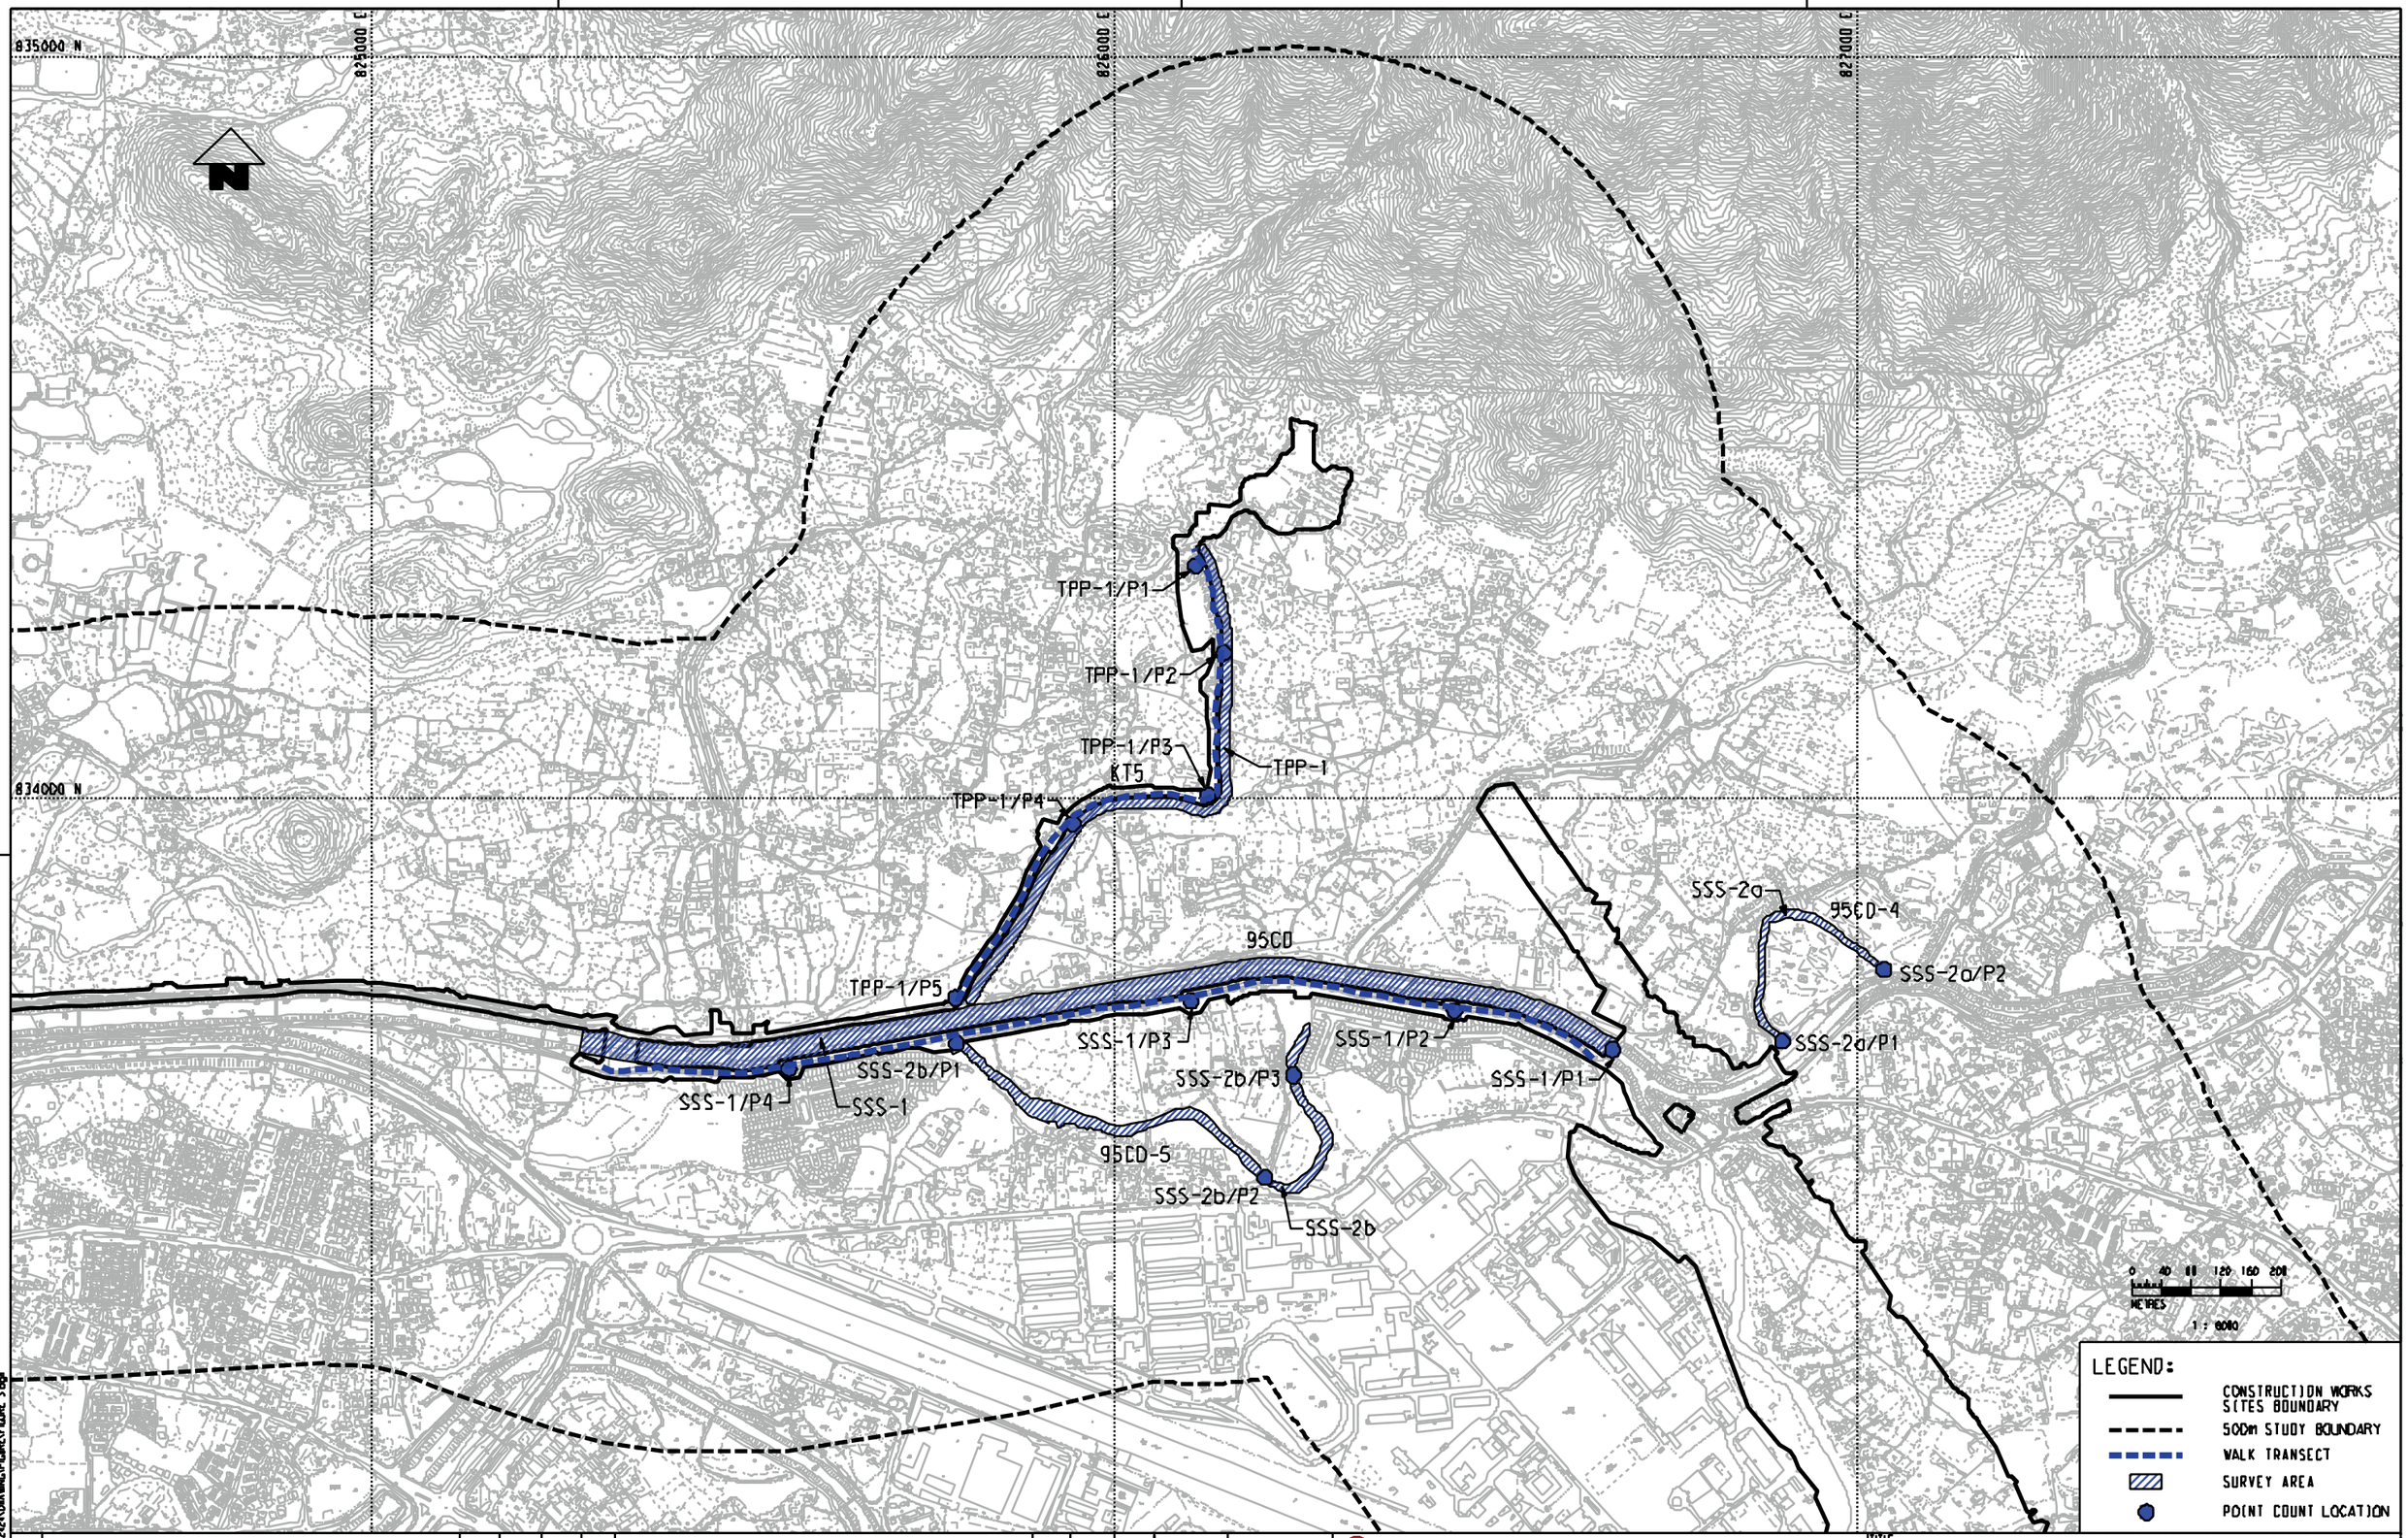

REV	DESCRIPTION	BY	DATE	APPROVED
REV	DESCRIPTION	BY	DATE	APPROVED

DRAWN	Y.JP
DESIGNED	TWF
CHECKED	K.CC
APPROVED	PL
DATE	14/SEP./2009

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
© MTR CORPORATION LIMITED 2008 COPYRIGHT IN RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE DRAWING / DOCUMENT OR ANY PART OF IT MAY BE MADE UNLESS PERMITTED BY LAW OR WITH THE PRIOR WRITTEN CONSENT OF MTR CORPORATION LIMITED.

MTR

EXPRESS RAIL LINK

ENDORSEMENT

AECOM

CADD REF FIGURE 3.dgn

TITLE

NOL / ERL-300

BASELINE BIRD SURVEY FOR EIA

PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR TPP-1, SSS-1,SSS-2a AND SSS-2b

SCALE 1 : 8000 (A3)

FIGURE NO. FIGURE 3

REV. -

PLOT DRW: c:\autocad\MTRYLO\DRIVER\NODEFLAS COLOUR.ctb
ADDED/MODIFIED BY: Cheryl
PLOTTED BY: 204-rm
FILENAME: P:\PROJECTS\60422\DIAGRAMS\FIGURE 3.dgn
19:13:40

827500 E
828000 E
828500 E
827000 E
833500 N
833000 N
832500 N
832000 N
831500 N

SSS-3

SSS-3/P1
SSS-3/P2
SSS-3/P3
SSS-3/P4
SSS-3/P5
SSS-3/P6
SSS-3/P7
SSS-3/P8
SSS-3/P9
SSS-3/P10
SSS-3/P11
SSS-3/P12

LEGEND:

- CONSTRUCTION WORKS SITES BOUNDARY
- 500m STUDY BOUNDARY
- WALK TRANSECT
- POINT COUNT LOCATION
- ACTIVE AGRICULTURE
- INACTIVE AGRICULTURE
- ACTIVE FISHPOND
- INACTIVE FISHPOND/POND
- REEDBED/FRESHWATER MARSH
- WATERCOURSE
- DRAINAGE CHANNEL
- GRASSLAND
- SEASONALLY WET GRASSLAND
- SECONDARY WOODLAND
- SHRUBLAND
- PLANTATION
- DEVELOPED AREA/WASTEGROUND

0 30 60 90 120 150
METRES
1 : 6000

PLOT DRV
MODELNAME
FILENAME: P:\mastmain\MTRPLOTDRIVER\WINDOWS\AS COLOUR.pltPLOTTED BY: CHWIYP 14/8/24
Default DATE: 2009-11
DATA\PROJECTS\60412621\PLOT\MRG\FIGURE\FIGURE 4.dgn

REV	DESCRIPTION	BY	DATE	APPROVED

REV	DESCRIPTION	BY	DATE	APPROVED

DRAWN	YJP
DESIGNED	TWF
CHECKED	KCC
APPROVED	PL
DATE	07/DEC./2009

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
© MTR CORPORATION (C.I.)TED) 2006 COPYRIGHT IN RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY THE MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE WHOLE OR ANY PART OF THIS DRAWING / DOCUMENT MAY BE MADE WITHOUT THE PRIOR WRITTEN CONSENT OF THE MTR CORPORATION LIMITED.

MTR

EXPRESS RAIL LINK

ORIGINATOR
AECOM

CADD REF.
FIGURE 4.dgn

TITLE
NOL / ERL-300
BASELINE BIRD SURVEY FOR EIA
PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR SSS-3

SCALE	FIGURE NO.	REV
1 : 6000 (A3)	FIGURE 4	-

827500 E
828000 E
828500 E
833500 N
833000 N
832500 N
832000 N
831500 N

TUW-1/P1
TUW-1/P2
TUW-1/P3
TUW-1/P4
TUW-1/P5
TUW-1/P6
TUW-1/P7
TUW-1

LEGEND:

- CONSTRUCTION WORKS SITES BOUNDARY
- 500m STUDY BOUNDARY
- WALK TRANSECT
- POINT COUNT LOCATION
- ACTIVE AGRICULTURE
- INACTIVE AGRICULTURE
- ACTIVE FISHPOND
- INACTIVE FISHPOND/POND
- REEDBED/FRESHWATER MARSH
- WATERCOURSE
- DRAINAGE CHANNEL
- GRASSLAND
- SEASONALLY WET GRASSLAND
- SECONDARY WOODLAND
- SHRUBLAND
- PLANTATION
- DEVELOPED AREA/WASTEGROUND

0 30 60 90 120 150
METRES
1 : 6000

PLOT DRV: P:\ustmaan\MTRPLOTDRIVER\WIN00RSV.AS COLOUR.pltr
MODELNAME: Default
PLTCHANGE: DATA\PROJECTS\60412621\PLOT\MXD\FIGURE 5.MXD
PLOTTED BY: CHWIYU 2009-11 14:54:44

REV	DESCRIPTION	BY	DATE	APPROVED	REV	DESCRIPTION	BY	DATE	APPROVED

DRAWN	YJP
DESIGNED	TWF
CHECKED	KCC
APPROVED	PL
DATE	07/DEC./2009

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
© MTR CORPORATION (LISTED) 2006 COPYRIGHT IN RESPECT OF THIS DRAWING IS OWNED BY THE MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE MARKING / DRAWING OR ANY PART BY WHATEVER MEANS IS PERMITTED WITHOUT THE PRIOR WRITTEN CONSENT OF THE MTR CORPORATION LIMITED.

MTR

EXPRESS RAIL LINK

ORIGINATOR: AECOM

CADD REF.: FIGURE 5.dgn

TITLE
NOL / ERL-300
BASELINE BIRD SURVEY FOR EIA
PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR TUW-1

SCALE	FIGURE NO.	REV
1 : 6000 (A3)	FIGURE 5	-

826000 E
827000 E
828000 E
829000 E
832000 N
833000 N
831000 N

TUW-2 and PHV-1/P2

TUW-2 and PHV-1/P1

TUW-2 AND PHV-1

LEGEND:

- CONSTRUCTION WORKS SITES BOUNDARY
- 500m STUDY BOUNDARY
- WALK TRANSECT
- SURVEY AREA
- POINT COUNT LOCATION

0 40 80 120 160 200
METRES
1 : 8000

REV	DESCRIPTION	BY	DATE	APPROVED
REV	DESCRIPTION	BY	DATE	APPROVED

DRAWN	CYG
DESIGNED	TWF
CHECKED	KCC
APPROVED	PL
DATE	07/DEC./2009

ON HCM SCALE DRAWINGS, ALL DIMENSIONS SHALL BE USED AS GIVEN.
© MTR CORPORATION LIMITED 2008 COPYRIGHT IN RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY MTR CORPORATION LIMITED OF HONG KONG. NO PERSON MAY DO ANY ACT WHICH INFRINGES, OR AUTHORISES OR PERMITS ANY INFRINGEMENT OF, ANY OF THE RIGHTS CONFERRED BY THE COPYRIGHT ORDINANCE IN RESPECT OF THIS DRAWING / DOCUMENT.

MTR

EXPRESS RAIL LINK

ORIGINATOR

AECOM

CADD REF FIGURE 6.dgn

TITLE

NOL / ERL-300

BASELINE BIRD SURVEY FOR EIA


PROPOSED SURVEY AREA, POINT COUNT LOCATION AND WALK TRANSECT FOR TUW-2 AND PHV-1

SCALE 1 : 8000 (A3)

FIGURE NO. FIGURE 6

REV. -

PLOT DWG: r:\submit\MTR\PLOTDRWG\WORDFILE\A3 COLOR.pdf
MODIFIED BY: Derfun
FILENAME: P:\PROJECTS\60042210\DRAWING\FIGURE 6.dgn
PLOTTED BY: TANG
2009-12
H:304

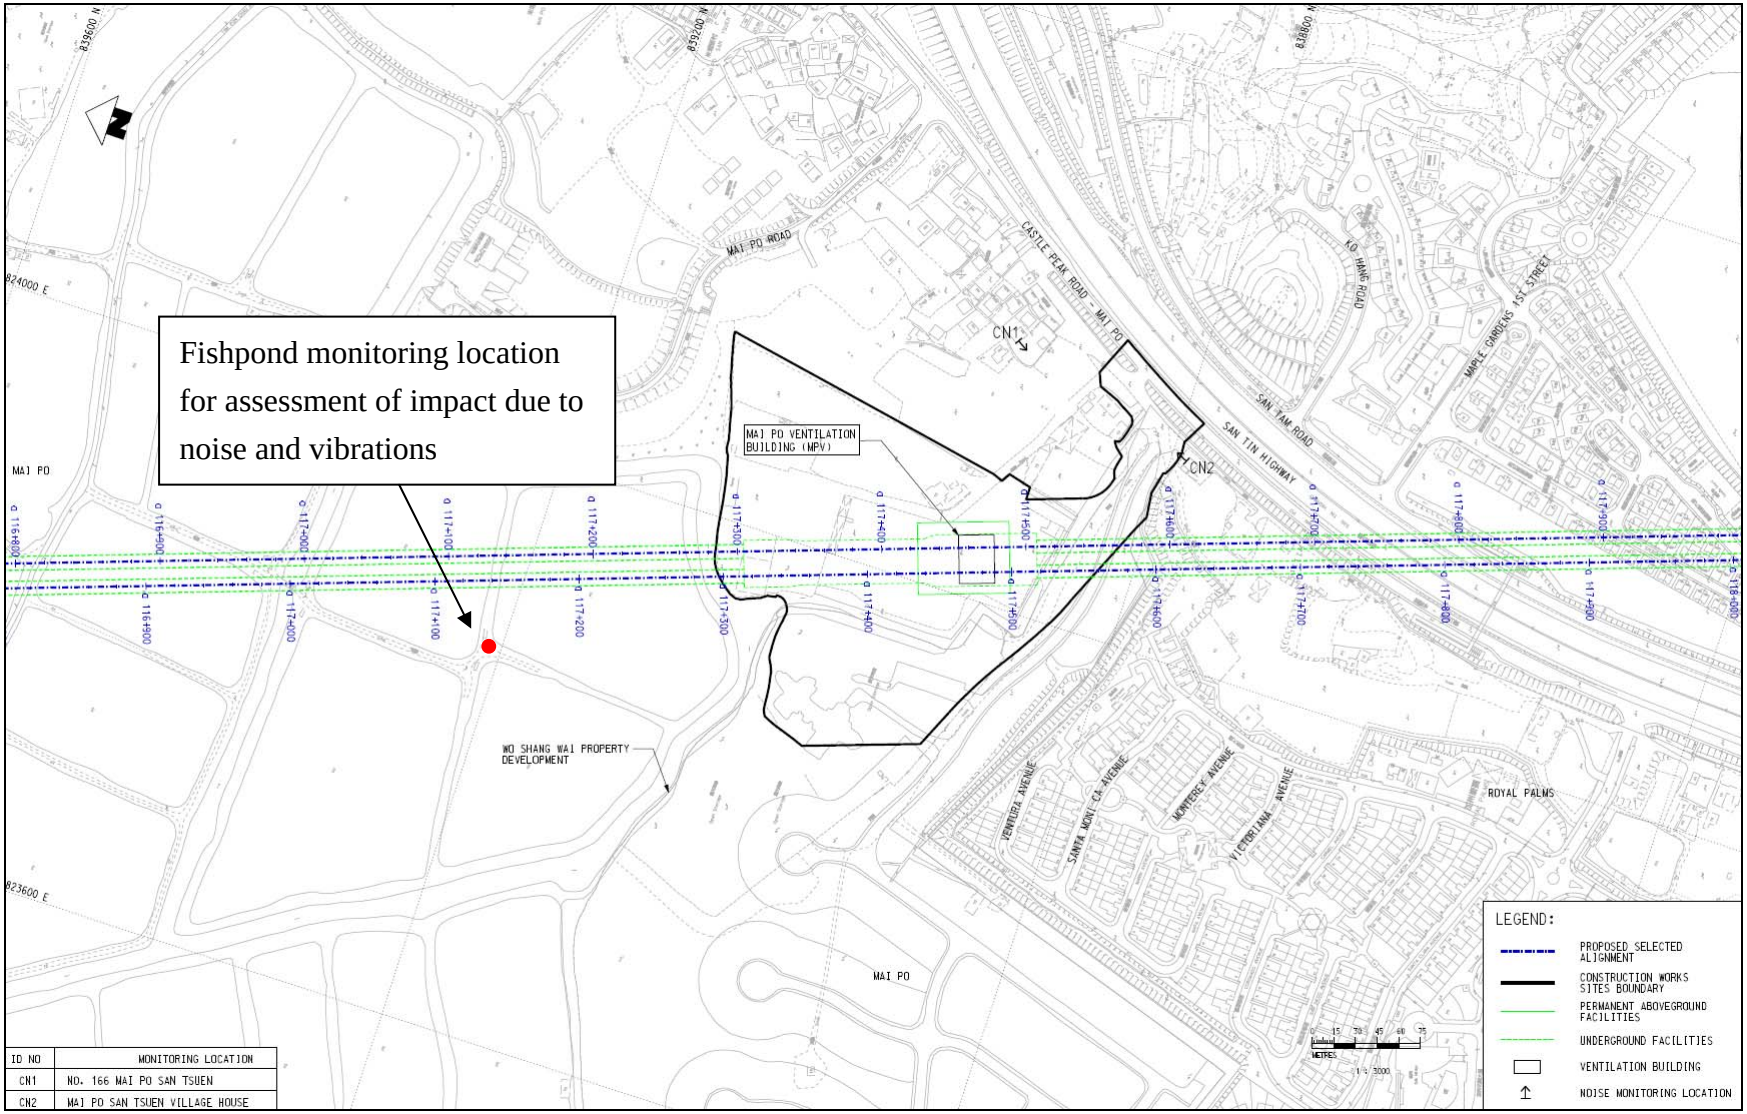

Fishpond monitoring location

Appendix E

Monitoring Schedule

Monitoring Schedule in the Next Reporting Month (01 Apr 2011 - 30 Apr 2011)

	CN1	CN2	CN3	CN4	CN5	CN6	CN7	CN8	CN9	CN10	CN11	CN12	CN13	CN14	CN15	CN16
Date	No. 142 Mai Po San Tsuen	Mai Po San Tsuen Village Hse	Yau Tam Mei Village House	Yau Tam Mei Village House	Kong Tai Road Village House	Kong Tai Road Village House	House 93, Seasons Villas	DD110 LOT 482, Wang Toi Shan	Leung Uk Tsuen Village House	Leung Uk Tsuen Squats	182B, Wang Toi Shan San Tsuen	630 Sheung Tsuen	No. 489H Tse Uk Tsuen	Tse Uk Tsuen	No. 305B - Sheung Tsuen San Tsuen Village	DD 114 LOT 1405 Sheung Tsuen
01-Apr-11								√				√	√	√		
02-Apr-11																
03-Apr-11																
04-Apr-11									√						√	√
05-Apr-11																
06-Apr-11			√	√		√				√						
07-Apr-11							√									
08-Apr-11	√	√			√			√			√	√	√	√		
09-Apr-11																
10-Apr-11																
11-Apr-11																√
12-Apr-11			√	√		√			√	√					√	
13-Apr-11		√					√									
14-Apr-11																
15-Apr-11	√				√			√			√	√	√	√		
16-Apr-11																
17-Apr-11																
18-Apr-11		√													√	√
19-Apr-11			√	√		√	√		√	√						
20-Apr-11																
21-Apr-11	√				√			√			√	√	√	√		
22-Apr-11																
23-Apr-11																
24-Apr-11																
25-Apr-11																
26-Apr-11		√		√					√	√					√	√
27-Apr-11			√			√	√									
28-Apr-11																
29-Apr-11	√				√			√			√	√	√	√		
30-Apr-11																

Monitoring Schedule in the Next Reporting Month (01 Apr 2011 - 30 Apr 2011)

	CN18	CN19	CN20	CN21	CN22	CN23	CN24	CN25	CN26	CN27	CN28	CN29	CN30	CN31	CN32	CN33	CN34
Date	Sau Shan House	Sun Fung Centre	VTC Kwai Chung	Po Leung Kuk Tong Nai Kan College	Block I, Lai Chi Kok Reception Centre	HKIVE Haking Wong Waterfront Annex	St. Andrew Primary School	St. Mary's Church Mok Hing Yiu College	Ying Wah College	Cheong Shun House, Nam Cheong Estate	Tower 6, Harbour Green	Yaumati Catholic Primary School	Man Cheong Street Refuse Collection Point	Tower 6, Sorrento	Tower 3, The Waterfront	Star Tower, The Arch	The Victoria Towers
01-Apr-11																	
02-Apr-11																	
03-Apr-11																	
04-Apr-11	√	√											√	√			
05-Apr-11																	
06-Apr-11						√			√		√				√		√
07-Apr-11			√				√	√		√						√	
08-Apr-11				√	√							√					
09-Apr-11																	
10-Apr-11																	
11-Apr-11	√	√															
12-Apr-11			√									√	√	√			
13-Apr-11						√					√						
14-Apr-11				√	√		√	√	√	√							
15-Apr-11															√	√	√
16-Apr-11																	
17-Apr-11																	
18-Apr-11	√	√															
19-Apr-11			√									√	√	√			
20-Apr-11						√			√		√				√	√	√
21-Apr-11				√	√		√	√		√							
22-Apr-11																	
23-Apr-11																	
24-Apr-11																	
25-Apr-11																	
26-Apr-11	√	√	√											√		√	
27-Apr-11						√					√	√	√				
28-Apr-11				√	√		√	√	√	√							√
29-Apr-11															√		
30-Apr-11																	

Monitoring Schedule in the Next Reporting Month (01 May 2011 - 31 May 2011)

	CN1	CN2	CN3	CN4	CN5	CN6	CN7	CN8	CN9	CN10	CN11	CN12	CN13	CN14	CN15	CN16
Date	No. 142 Mai Po San Tsuen	Mai Po San Tsuen Village Hse	Yau Tam Mei Village House	Yau Tam Mei Village House	Kong Tai Road Village House	Kong Tai Road Village House	House 93, Seasons Villas	DD110 LOT 482, Wang Toi Shan	Leung Uk Tsuen Village House	Leung Uk Tsuen Squats	182B, Wang Toi Shan San Tsuen	630 Sheung Tsuen	No. 489H Tse Uk Tsuen	Tse Uk Tsuen	No. 305B - Sheung Tsuen San Tsuen Village	DD 114 LOT 1405 Sheung Tsuen
01-May-11																
02-May-11																
03-May-11																
04-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
05-May-11																
06-May-11																
07-May-11																
08-May-11																
09-May-11																
10-May-11																
11-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
12-May-11																
13-May-11																
14-May-11																
15-May-11																
16-May-11																
17-May-11																
18-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
19-May-11																
20-May-11																
21-May-11																
22-May-11																
23-May-11																
24-May-11																
25-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
26-May-11																
27-May-11																
28-May-11																
29-May-11																
30-May-11																
31-May-11																

Monitoring Schedule in the Next Reporting Month (01 May 2011 - 31 May 2011)

	CN18	CN19	CN20	CN21	CN22	CN23	CN24	CN25	CN26	CN27	CN28	CN29	CN30	CN31	CN32	CN33	CN34
Date	Sau Shan House	Sun Fung Centre	VTC Kwai Chung	Po Leung Kuk Tong Nai Kan College	Block I, Lai Chi Kok Reception Centre	HKIVE Haking Wong Waterfront Annex	St. Andrew Primary School	St. Mary's Church Mok Hing Yiu College	Ying Wah College	Cheong Shun House, Nam Cheong Estate	Tower 6, Harbour Green	Yaumati Catholic Primary School	Man Cheong Street Refuse Collection Point	Tower 6, Sorrento	Tower 3, The Waterfront	Star Tower, The Arch	The Victoria Towers
01-May-11																	
02-May-11																	
03-May-11																	
04-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
05-May-11																	
06-May-11																	
07-May-11																	
08-May-11																	
09-May-11																	
10-May-11																	
11-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
12-May-11																	
13-May-11																	
14-May-11																	
15-May-11																	
16-May-11																	
17-May-11																	
18-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
19-May-11																	
20-May-11																	
21-May-11																	
22-May-11																	
23-May-11																	
24-May-11																	
25-May-11	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√	√
26-May-11																	
27-May-11																	
28-May-11																	
29-May-11																	
30-May-11																	
31-May-11																	

Actual Construction Dust (24-hr TSP) Impact Monitoring Schedule - April 2011

Note 1: **TSP** denotes Total Suspended Particulate

Apr-2011						
Sunday	**Monday**	**Tuesday**	**Wednesday**	**Thursday**	**Friday**	**Saturday**
					1 AM11, AM12, AM13, AM14, AM15, AM16, AM17	2 AM1, AM2, AM4, AM9, AM10
3	4 AM3, AM5, AM6, AM7, AM8	5	6 AM11, AM12, AM13, AM14, AM15, AM16, AM17	7	8 AM1, AM2, AM4, AM9, AM10	9 AM3, AM5, AM6, AM7, AM8
10	11 AM11, AM12, AM13, AM14, AM15, AM16	12 AM17[#]	13	14 AM1, AM2, AM4, AM9, AM10	15 AM3, AM5, AM6, AM7, AM8	16 AM11, AM12, AM13, AM14, AM15, AM16, AM17
17	18	19	20 AM1, AM2, AM3, AM4, AM5, AM6, AM7, AM8, AM9, AM10	21 AM11, AM12, AM13, AM14, AM15, AM16, AM17	22	23
24	25	26 AM1, AM2, AM3, AM4, AM5, AM6, AM7, AM8, AM9, AM10	27 AM11, AM12, AM13, AM14, AM15, AM16, AM17	28	29 AM1, AM2, AM4, AM9, AM10	30 AM3, AM5, AM6, AM7, AM8

[#] 24-hr TSP impact monitoring for AM17 was proposed from 11 April 2011 to 12 April 2011 due to power supply shortage

Tentative Construction Dust (24-hr TSP) Impact Monitoring Schedule - May 2011

Note 1: **TSP** denotes Total Suspended Particulate

May-2011						
Sunday	**Monday**	**Tuesday**	**Wednesday**	**Thursday**	**Friday**	**Saturday**
1	2	3 AM11, AM12, AM13, AM14, AM15, AM16, AM17	4	5 AM1, AM2, AM4, AM9, AM10	6 AM3, AM5, AM6, AM7, AM8	7
8	9 AM11, AM12, AM13, AM14, AM15, AM16, AM17	10	11 AM1, AM2, AM4, AM9, AM10	12 AM3, AM5, AM6, AM7, AM8	13	14 AM11, AM12, AM13, AM14, AM15, AM16, AM17
15	16	17 AM1, AM2, AM4, AM9, AM10	18 AM3, AM5, AM6, AM7, AM8	19	20 AM11, AM12, AM13, AM14, AM15, AM16, AM17	21
22	23 AM1, AM2, AM4, AM9, AM10	24 AM3, AM5, AM6, AM7, AM8	25	26 AM11, AM12, AM13, AM14, AM15, AM16, AM17	27	28 AM1, AM2, AM4, AM9, AM10
29	30 AM3, AM5, AM6, AM7, AM8	31				

Appendix E Monitoring Schedule

Works Area	Survey Site	Date of Survey in April 2011	Tentative Date of Survey in May 2011
MPV	MPV-1	12 April 2011	9 May 2011
Access road leading to TPP	TPP-1	12 April 2011	9 May 2011
Access road leading to TPP	TPP-2	12 April 2011	9 May 2011
Access road leading to TPP	TPP-3	12 April 2011	9 May 2011
Access road leading to SSS / ERS	SSS-2a	12 April 2011	Monthly monitoring to be commenced subject to construction programme
Access road leading to SSS / ERS	SSS-3	19 April 2011	12 May 2011
TUW	TUW-1	19 April 2011	12 May 2011
TUW	TUW-2 (grouped with PHV-1 due to overlapping of survey area	19 April 2011	12 May 2011
PHV	PHV-1 (grouped with TUW-2 due to overlapping of survey area)	19 April 2011	12 May 2011

Appendix F

Graphical Plots of Monitoring Results

APPENDIX F: Noise Monitoring Results

- CN1

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	66	75	N
15/04/2011	66	75	N
21/04/2011	65	75	N
29/04/2011	67	75	N

- CN2

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	66	75	N
13/04/2011	67	75	N
18/04/2011	68	75	N
26/04/2011	68	75	N

- CN3

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	54	75	N
12/04/2011	55	75	N
19/04/2011	55	75	N
27/04/2011	58	75	N

- CN4

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	47	75	N
12/04/2011	60	75	N
19/04/2011	59	75	N
26/04/2011	54	75	N

- CN5

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	71	75	N
15/04/2011	73	75	N
21/04/2011	77	75	Y
29/04/2011	74	75	N

- CN6

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	61	75	N
12/04/2011	60	75	N
19/04/2011	60	75	N
27/04/2011	66	75	N

- CN7

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	66	75	N
13/04/2011	62	75	N
19/04/2011	63	75	N
27/04/2011	69	75	N

- CN8

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
01/04/2011	70	75	N
08/04/2011	73	75	N
15/04/2011	69	75	N
21/04/2011	70	75	N
29/04/2011	75	75	N

- CN9

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	69	75	N
12/04/2011	66	75	N
19/04/2011	60	75	N
26/04/2011	62	75	N

- CN10

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	56	75	N
12/04/2011	69	75	N
19/04/2011	59	75	N
26/04/2011	57	75	N

- CN11

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	68	75	N
15/04/2011	54	75	N
21/04/2011	65	75	N
29/04/2011	62	75	N

- CN12

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
01/04/2011	62	75	N
08/04/2011	69	75	N
15/04/2011	60	75	N
21/04/2011	68	75	N
29/04/2011	57	75	N

APPENDIX F: Noise Monitoring Results

- CN13

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
01/04/2011	64	75	N
08/04/2011	66	75	N
15/04/2011	57	75	N
21/04/2011	65	75	N
29/04/2011	57	75	N

- CN14

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
01/04/2011	57	75	N
08/04/2011	66	75	N
15/04/2011	58	75	N
21/04/2011	58	75	N
29/04/2011	61	75	N

- CN15

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	68	75	N
12/04/2011	71	75	N
19/04/2011	71	75	N
26/04/2011	75	75	N

- CN16

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	57	75	N
11/04/2011	54	75	N
18/04/2011	62	75	N
26/04/2011	56	75	N

- CN18

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	63	75	N
11/04/2011	70	75	N
18/04/2011	72	75	N
26/04/2011	71	75	N

- CN19

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	75	75	N
11/04/2011	69	75	N
18/04/2011	72	75	N
26/04/2011	60	75	N

- CN20

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	70	75	N
12/04/2011	71	75	N
19/04/2011	73	75	N
26/04/2011	71	75	N

- CN21

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	69	70	N
14/04/2011	69	70	N
21/04/2011	69	70	N
28/04/2011	69	70	N

- CN22

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	72	75	N
14/04/2011	73	75	N
21/04/2011	73	75	N
28/04/2011	73	75	N

- CN23

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	78	70	Y
13/04/2011	77	70	Y
20/04/2011	71	70	Y
27/04/2011	76	70	Y

Note:

- Impact monitoring at Tsuen Wan Lutheran School (CN 17) had been temporarily suspended since December 2010 due to school closure. Monitoring at this location will be resumed subject to confirmation of school operation or other noise sensitive use at CN 17.
- A correction factor has been applied at CN19 to take into account the noise barrier effect. The correction factor was agreed with IEC according to Section 3.11 of the EM&A Manual.
- Noise limit level of CN21, CN24, CN25, CN26 & CN29, which are school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.
- Exceedance at CN 23 on 20 Apr 2011 was not considered valid due to no school day.

APPENDIX F: Noise Monitoring Results

- CN24

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	68	70	N
14/04/2011	65	70	N
21/04/2011	68	70	N
28/04/2011	67	70	N

- CN25

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	66	65	Y
14/04/2011	57	65	N
21/04/2011	70	70	N
28/04/2011	69	70	N

- CN26

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	68	70	N
14/04/2011	67	70	N
20/04/2011	68	70	N
28/04/2011	70	70	N

- CN27

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	65	75	N
14/04/2011	65	75	N
21/04/2011	69	75	N
28/04/2011	65	75	N

- CN28

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	71	75	N
13/04/2011	73	75	N
20/04/2011	71	75	N
27/04/2011	73	75	N

- CN29

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
08/04/2011	68	70	N
12/04/2011	70	70	N
19/04/2011	67	70	N
27/04/2011	67	70	N

- CN30

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	71	75	N
12/04/2011	71	75	N
19/04/2011	71	75	N
27/04/2011	75	75	N

- CN31

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
04/04/2011	74	75	N
12/04/2011	74	75	N
19/04/2011	75	75	N
26/04/2011	74	75	N

- CN32

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	83	75	Y
15/04/2011	75	75	N
20/04/2011	82	75	Y
29/04/2011	79	75	Y


- CN33


Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
07/04/2011	78	75	Y
15/04/2011	74	75	N
20/04/2011	75	75	N
26/04/2011	75	75	N


- CN34

Date	Noise Monitoring Results	Limit Level	Exceedance?
	Leq, dB(A)	Leq, dB(A)	
06/04/2011	73	75	N
15/04/2011	73	75	N
20/04/2011	73	75	N
28/04/2011	72	75	N


Note:
- Noise limit level of CN21, CN24, CN25, CN26 & CN29, which are school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.

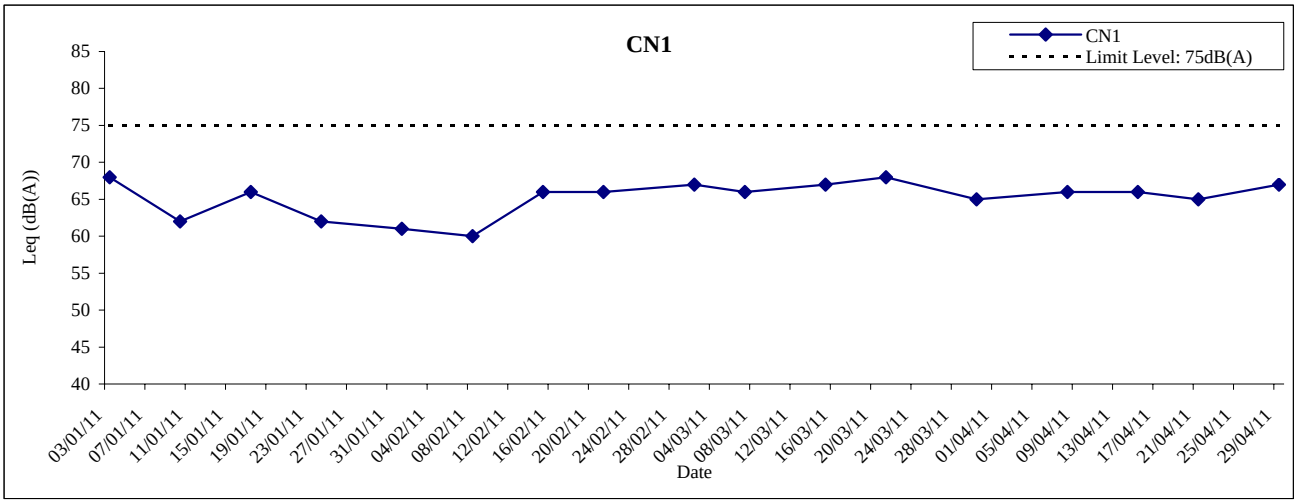


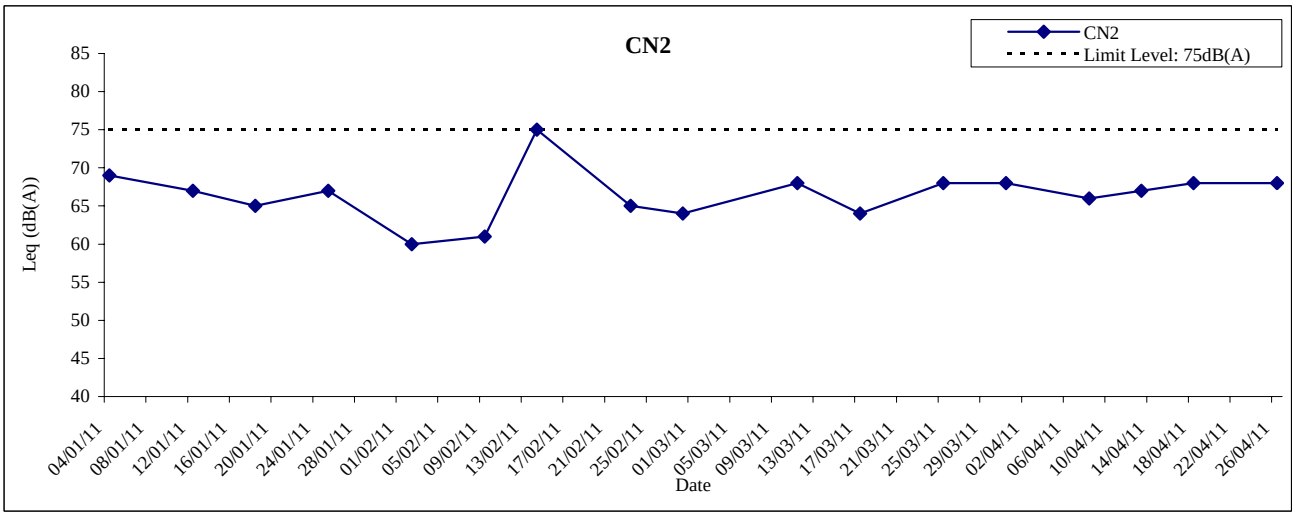


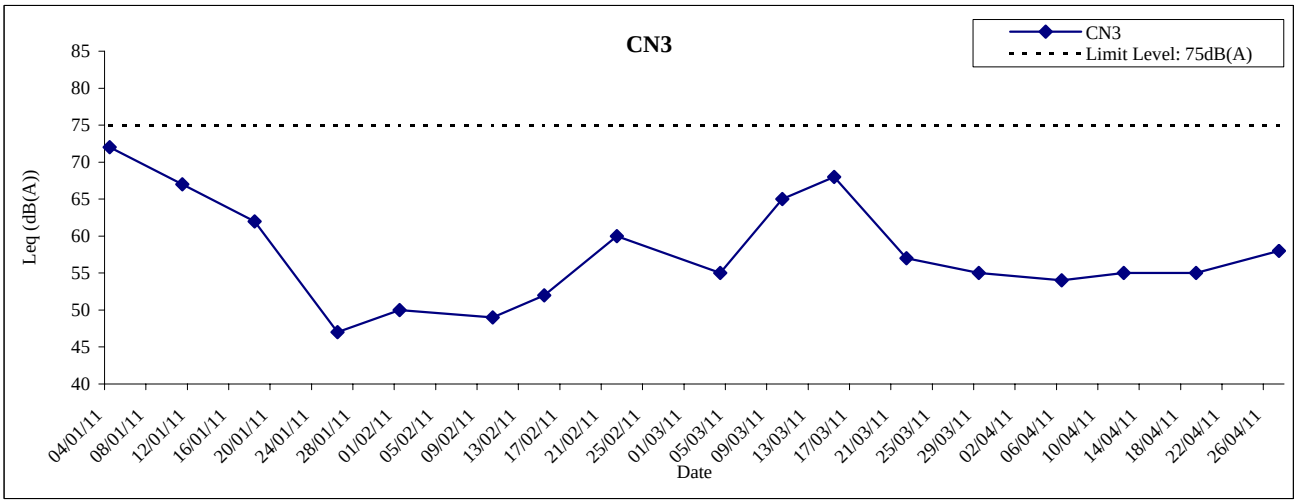


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN1, CN2 and CN3**	**Date**	**2011**
		APPENDIX	**F**

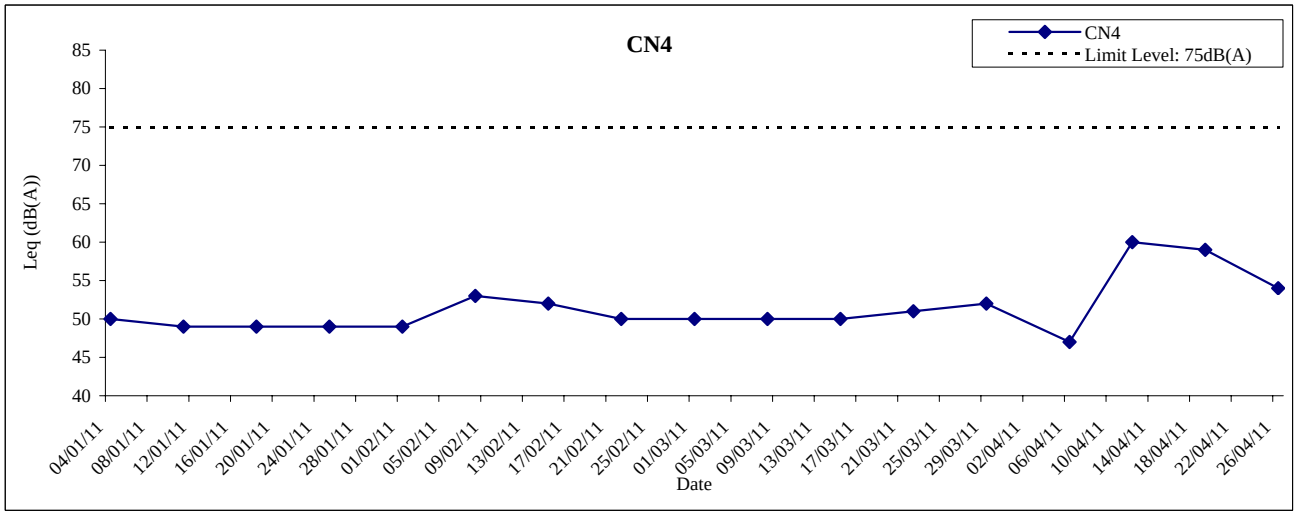


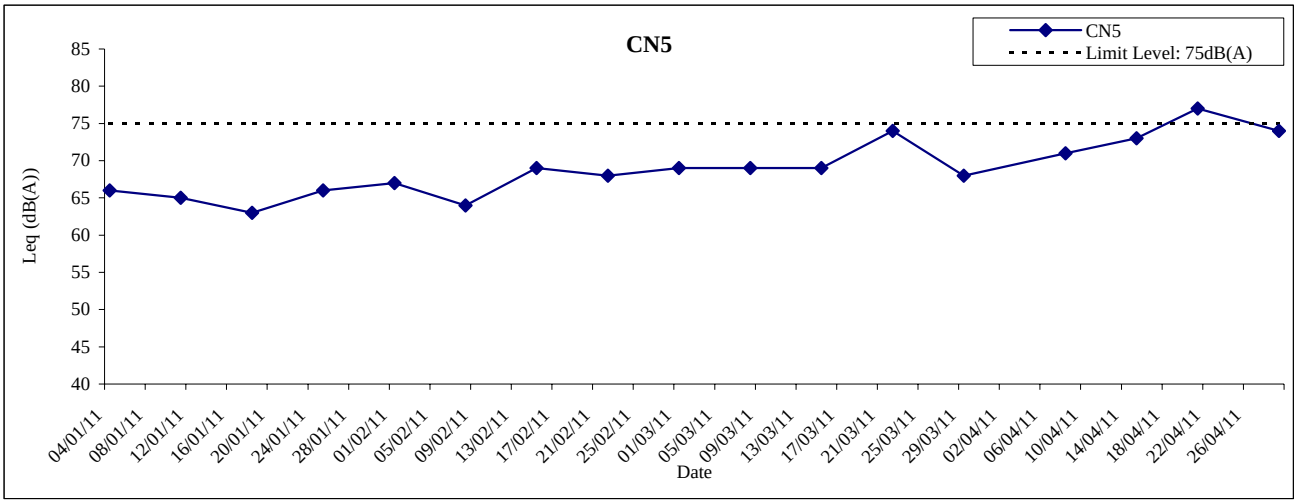


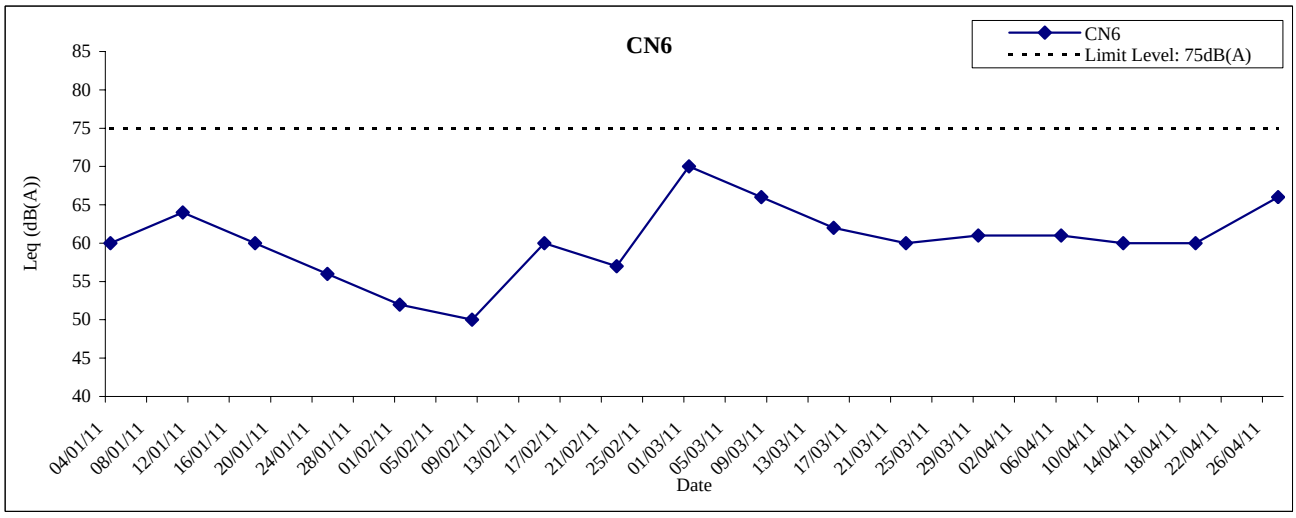


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN4, CN5 and CN6**	**Date**	**2011**
		APPENDIX	**F**

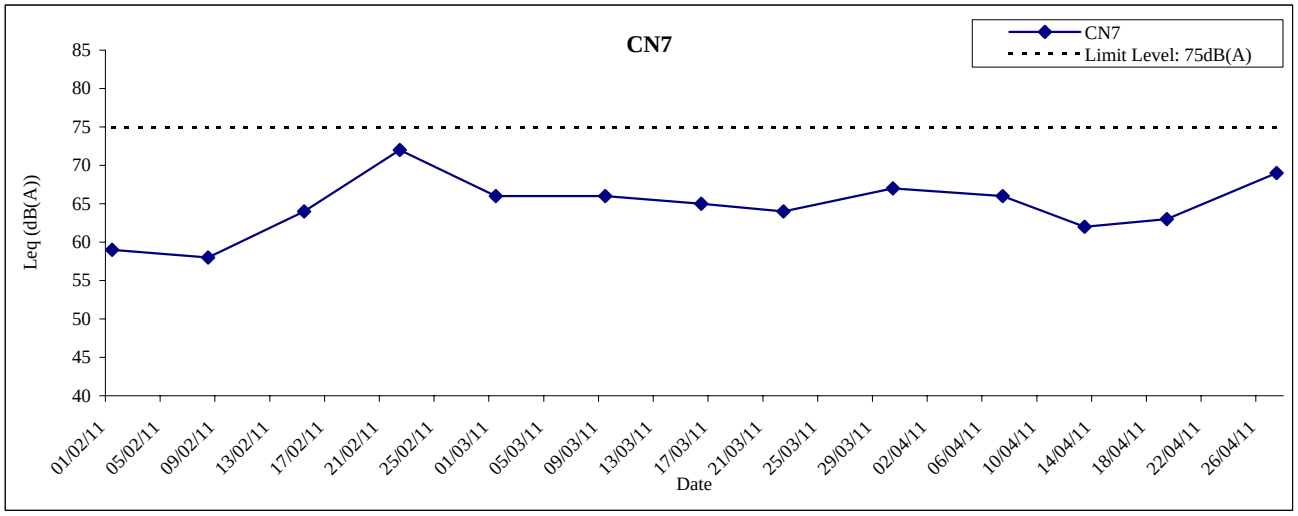


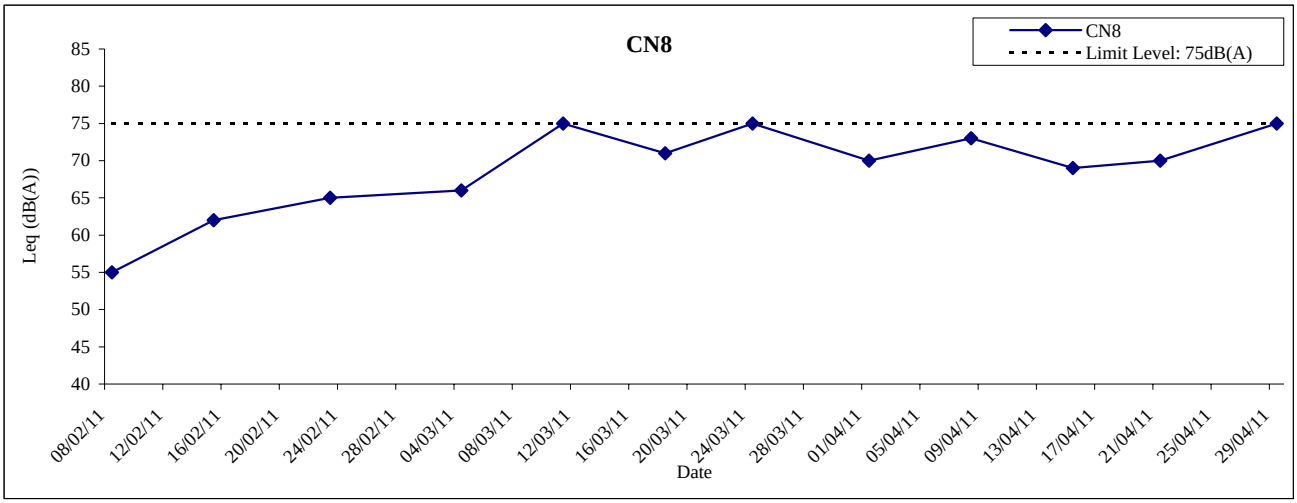


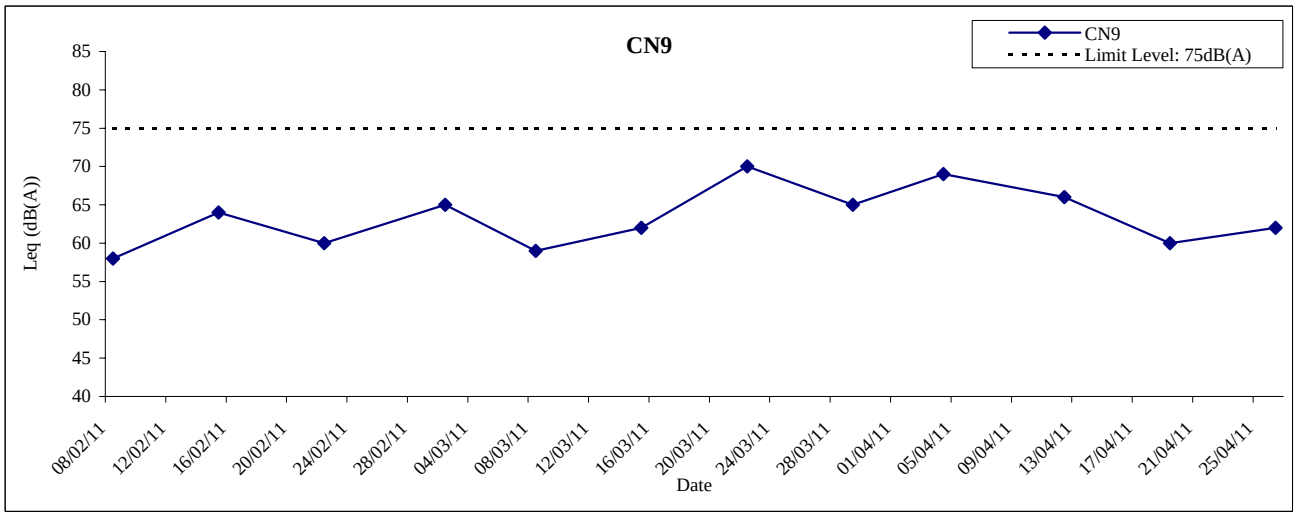


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN7, CN8 and CN9**	**Date**	**2011**
		APPENDIX	**F**

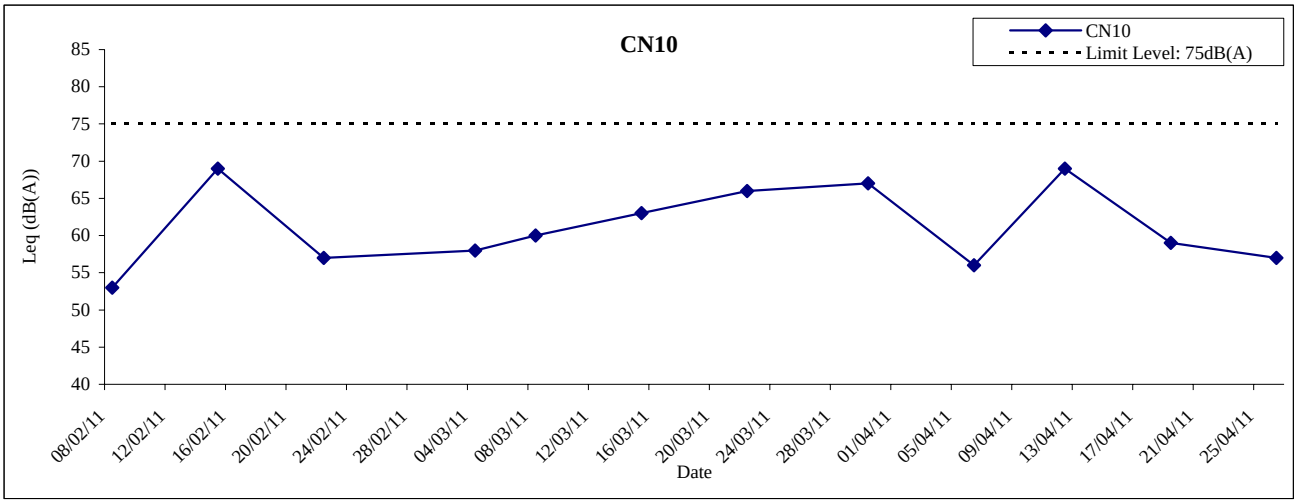


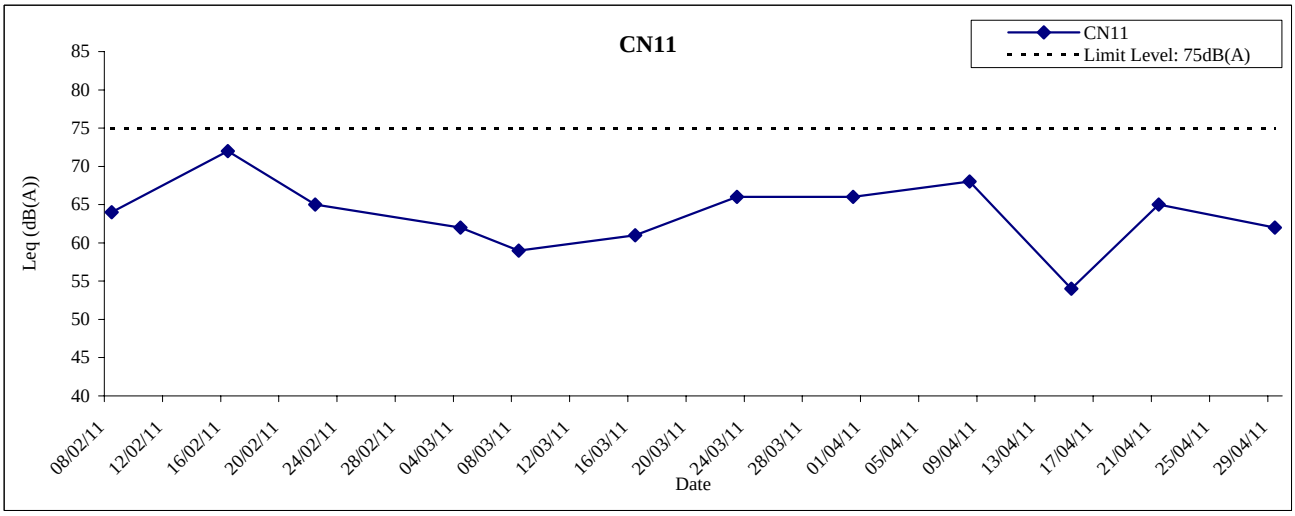


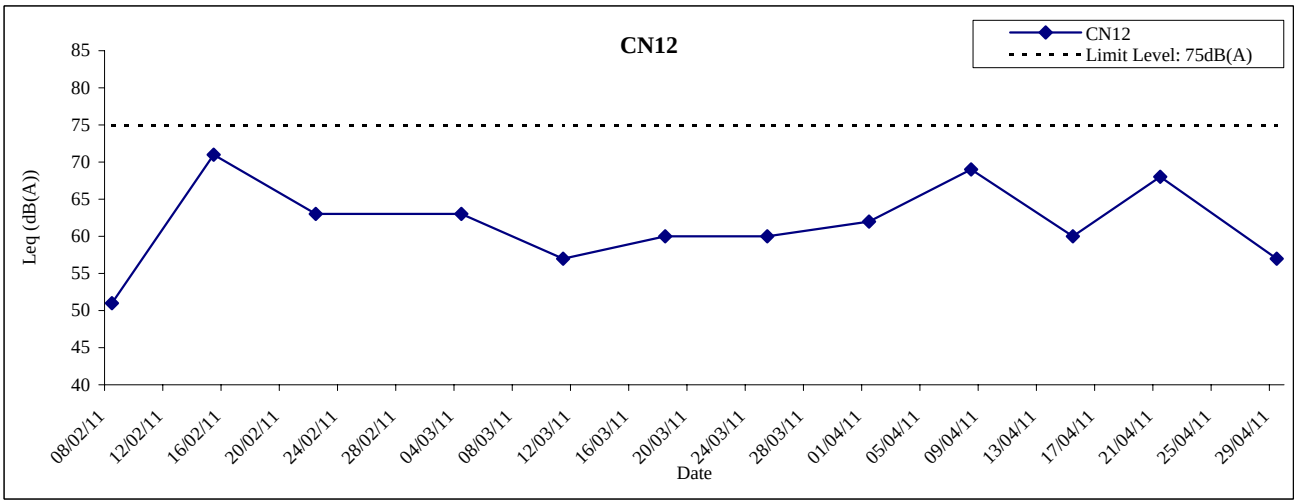


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN10, CN11 and CN12**	**Date**	**2011**
		APPENDIX	**F**

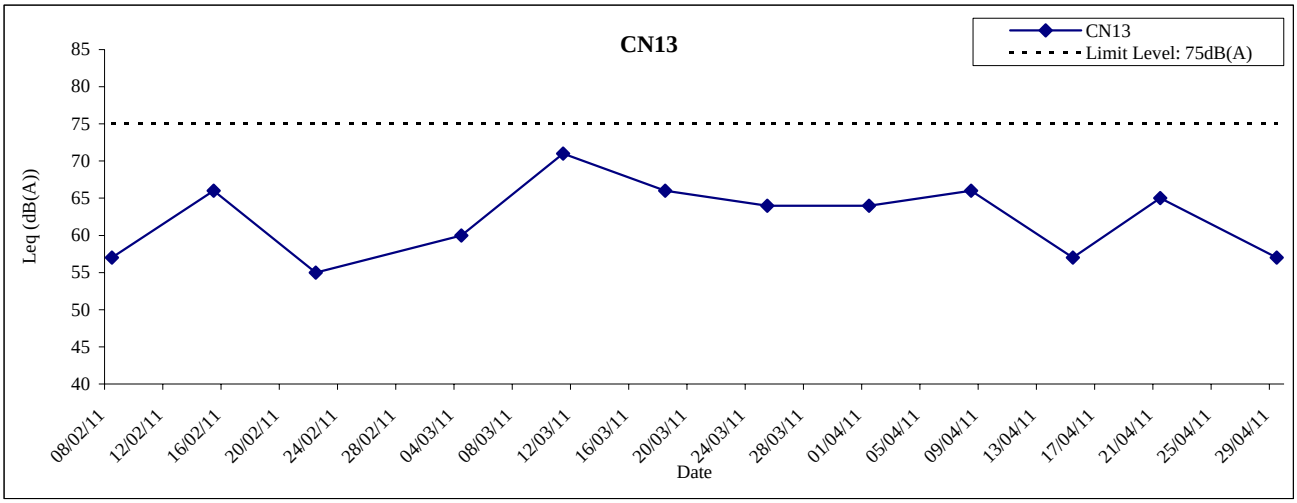


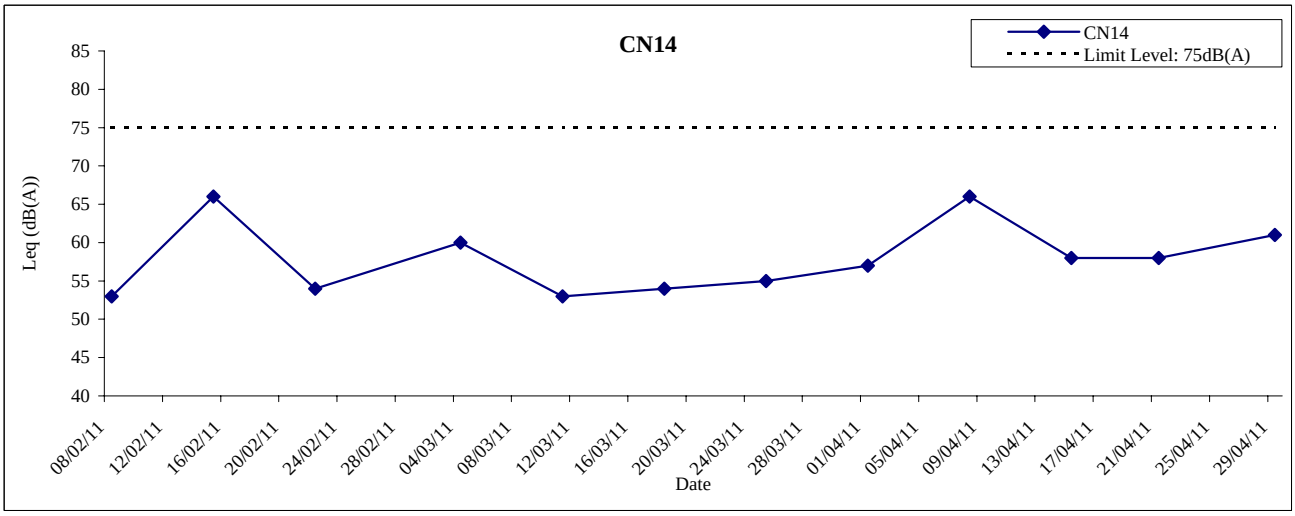


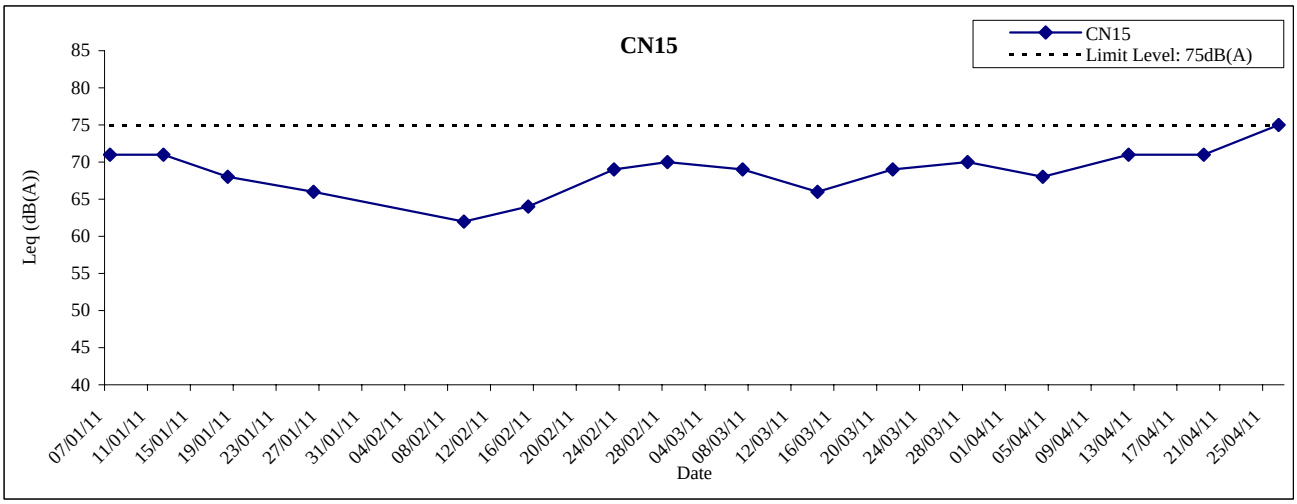

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN13, CN14 and CN15**	**Date**	**2011**
		APPENDIX	**F**

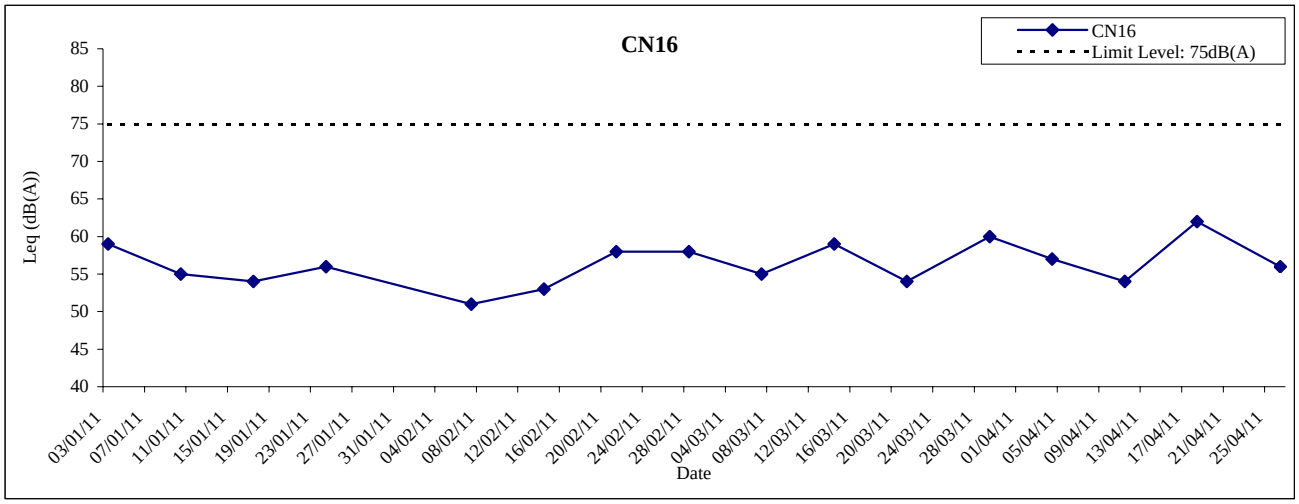

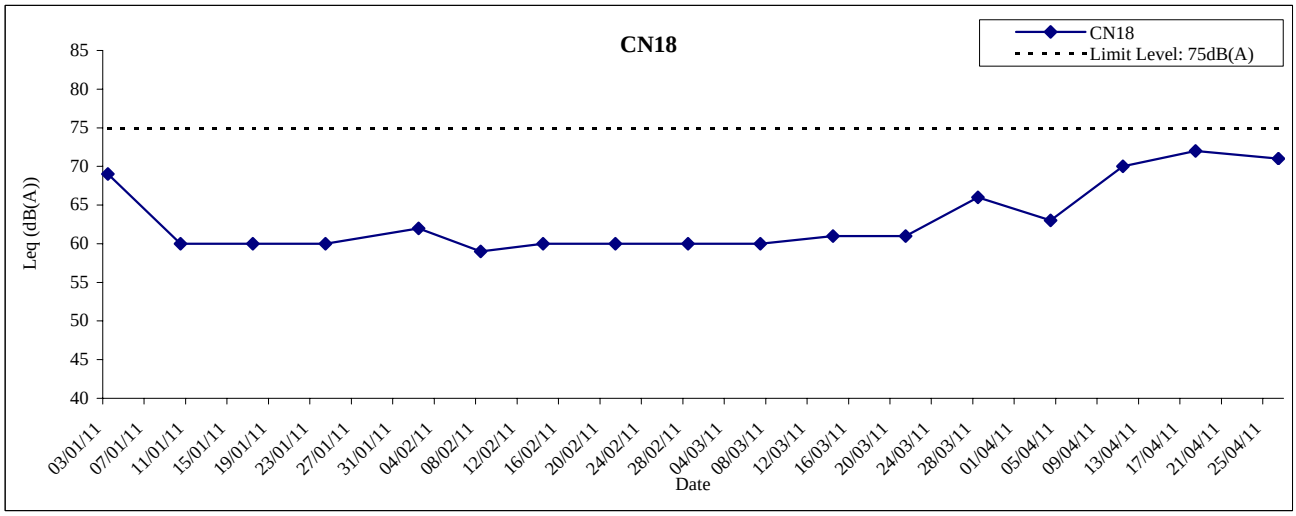


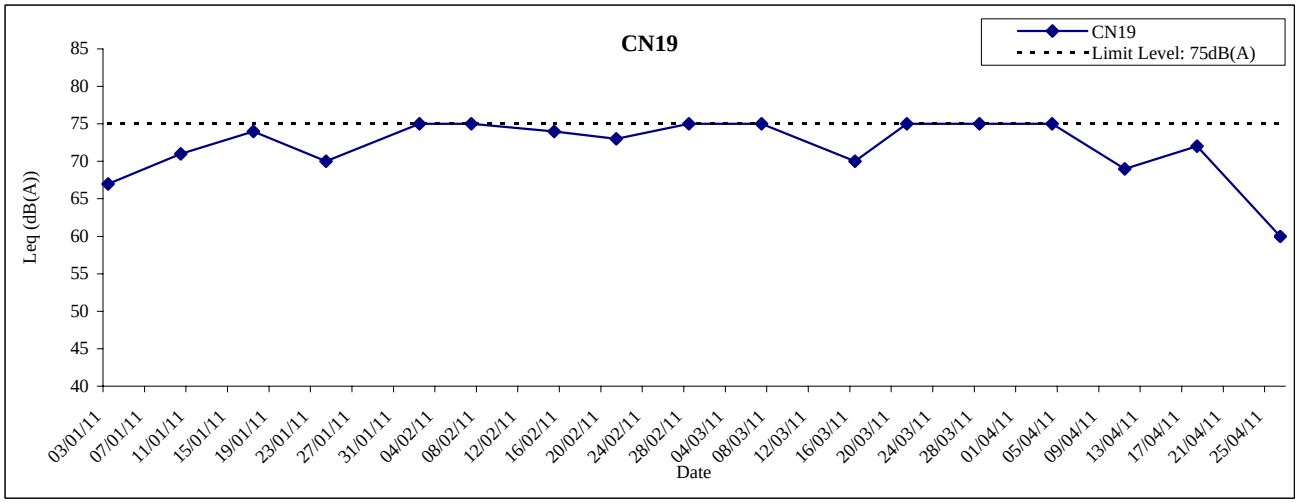



Remarks:

A correction factor has been applied at CN19 to take into account the noise barrier effect. The correction factor was agreed with IEC according to Section 3.11 of the EM&A Manual.

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN16, CN18 and CN19**	**Date**	**2011**
		APPENDIX	**F**

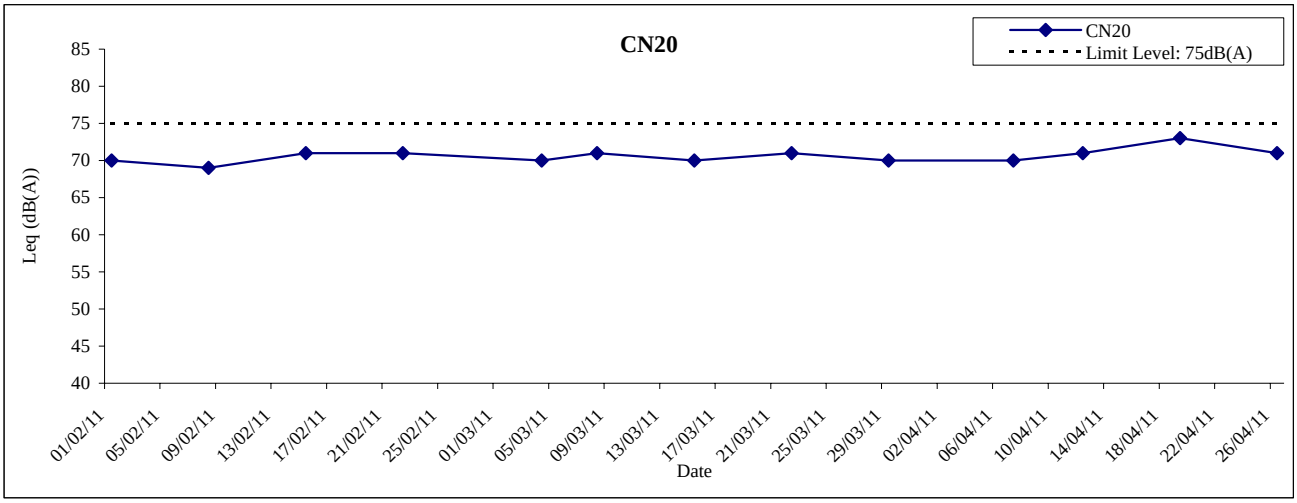


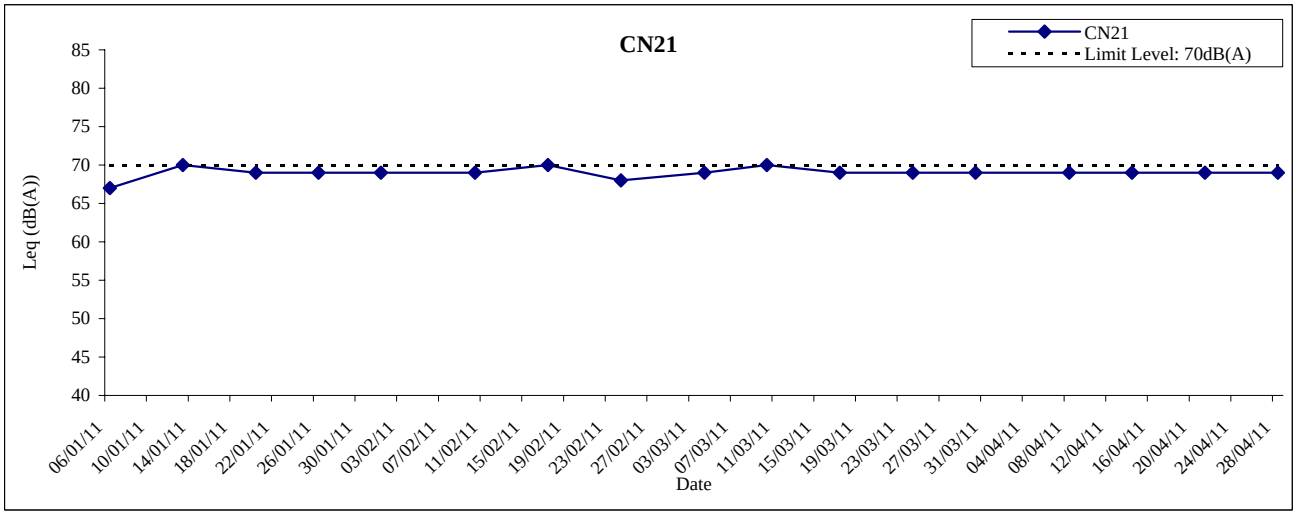


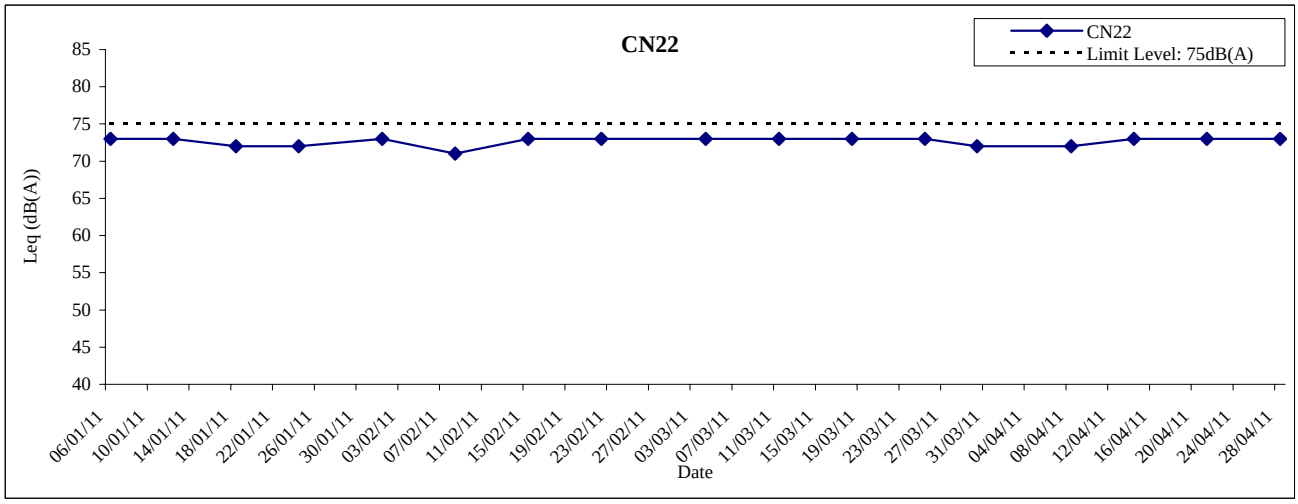


Remarks:
Noise limit level of CN21, which is school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN21, CN22 and CN23**	**Date**	**2011**
		APPENDIX	**F**

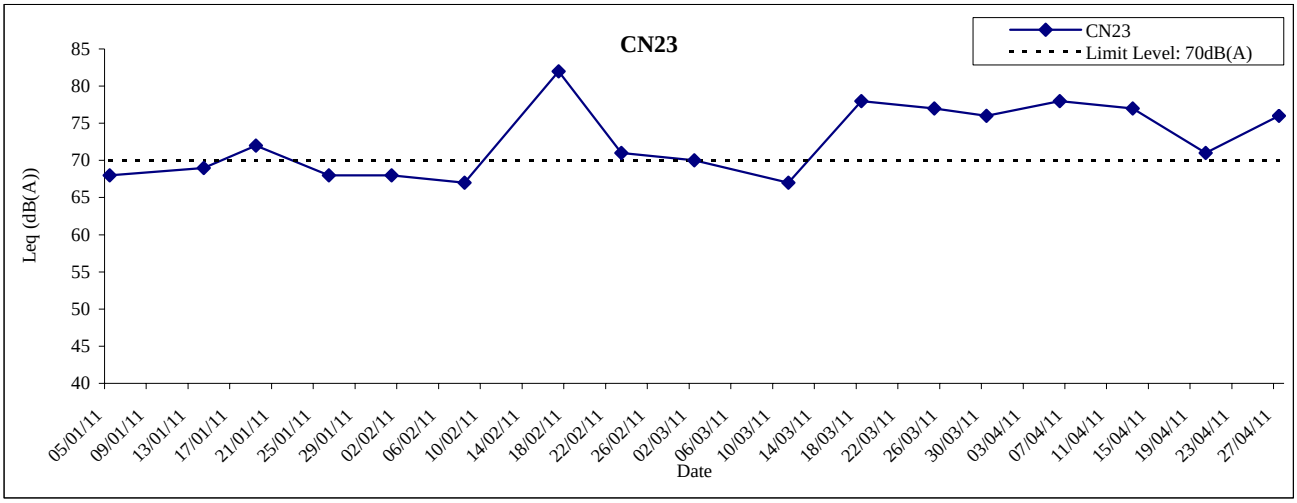


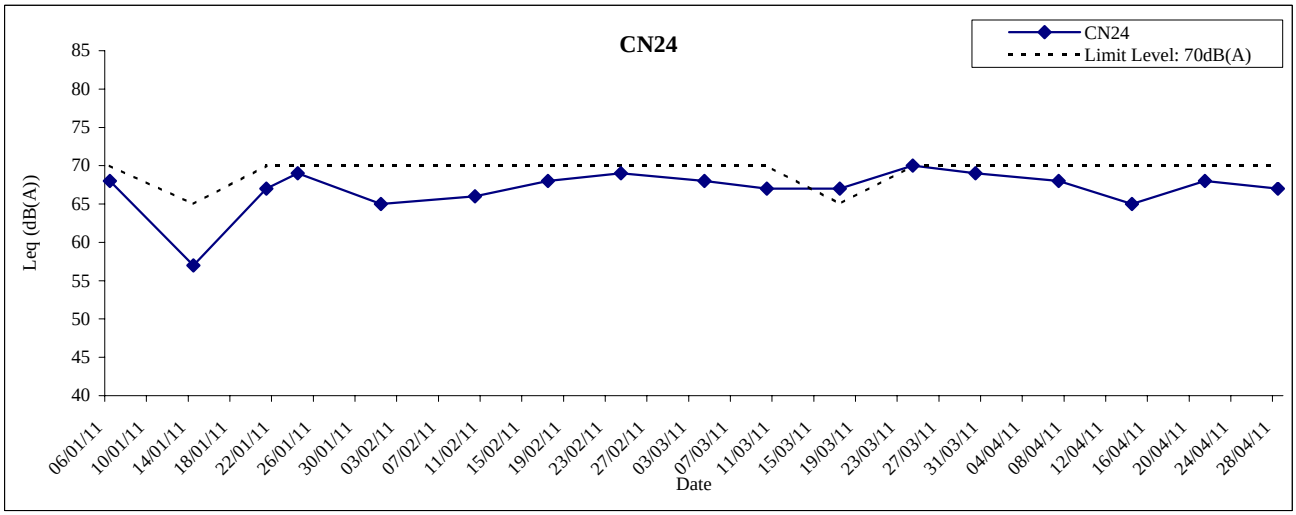


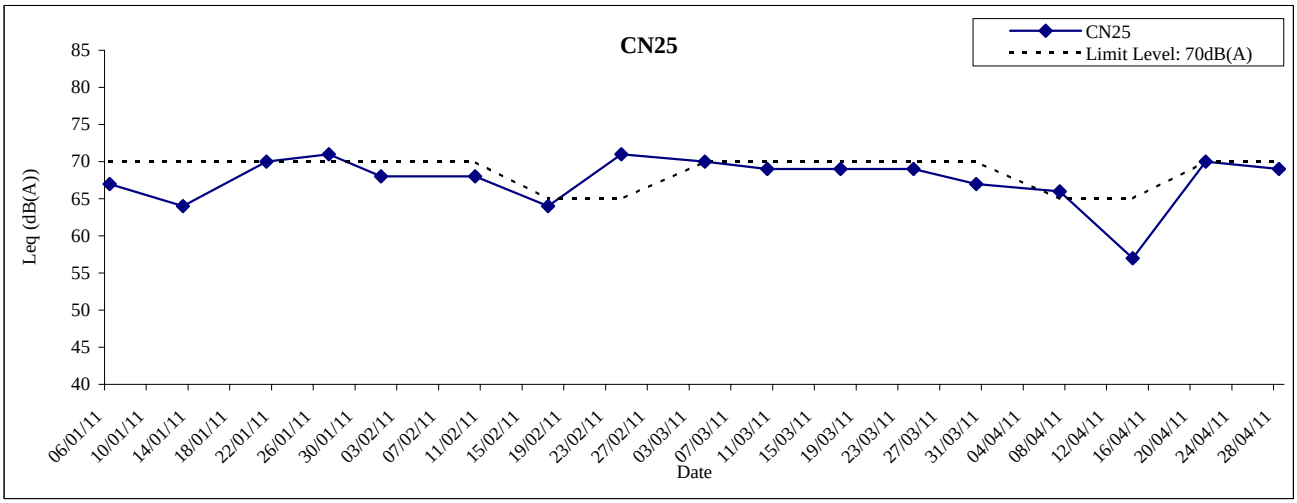


Remarks:
-Noise limit level of CN24 & CN25, which are school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.
-Exceedance at CN 23 on 20 Apr 2011 was not considered valid due to no school day.

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN23, CN24 and CN25**	**Date**	**2011**
		APPENDIX	**F**

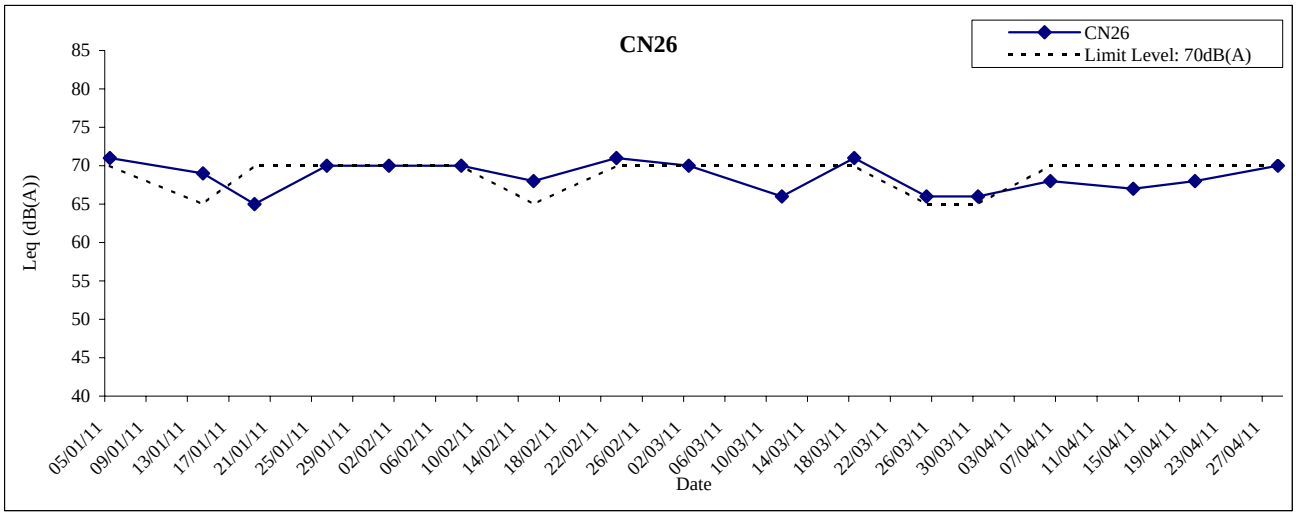


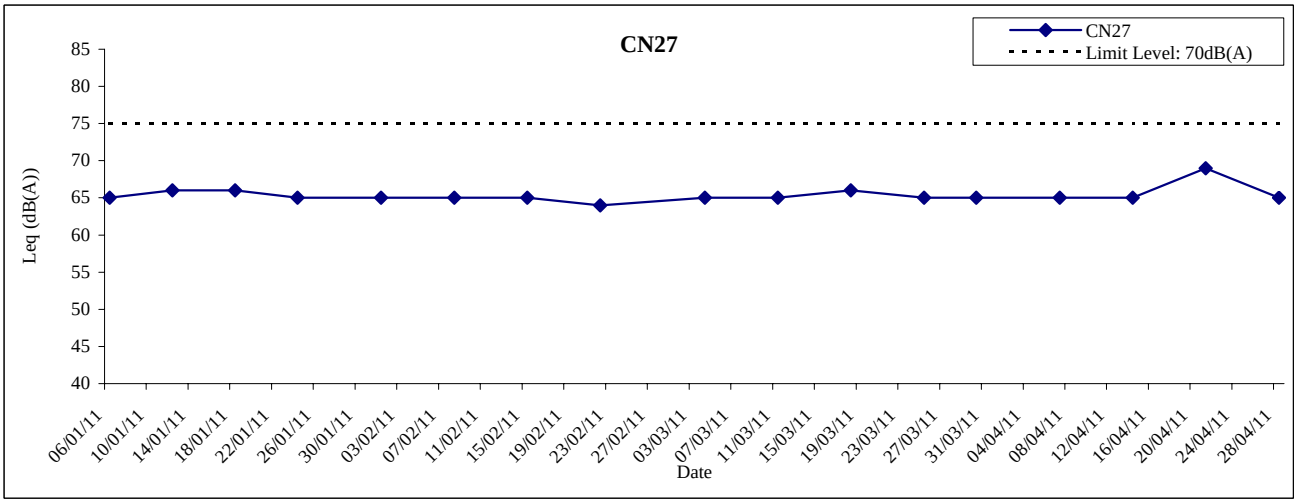


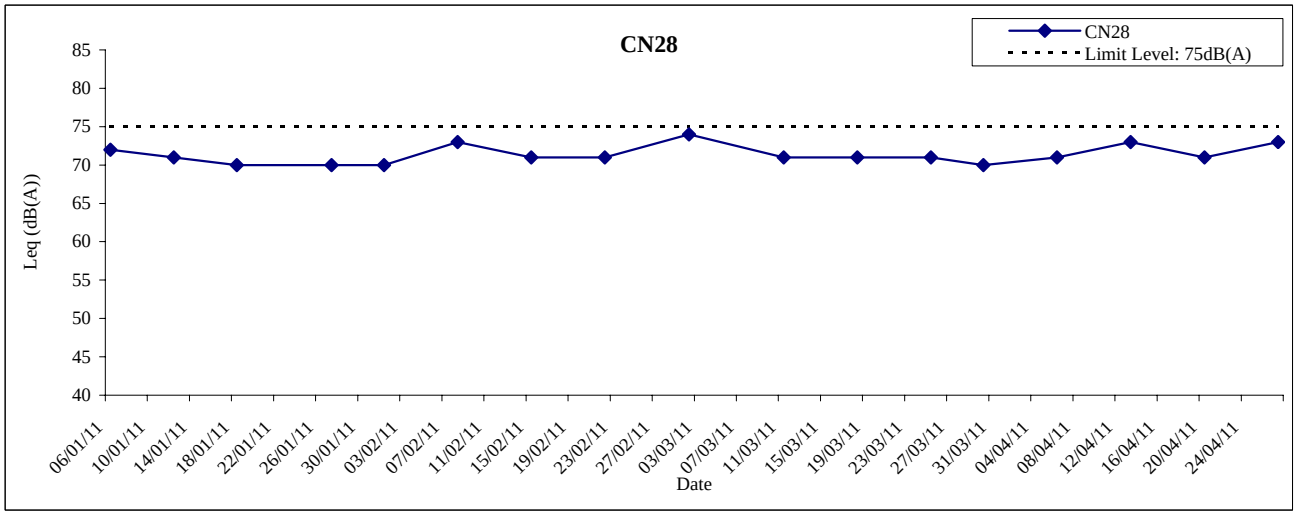


Remarks:
Noise limit level of CN26, which is school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN26, CN27 and CN28**	**Date**	**2011**
		APPENDIX	**F**

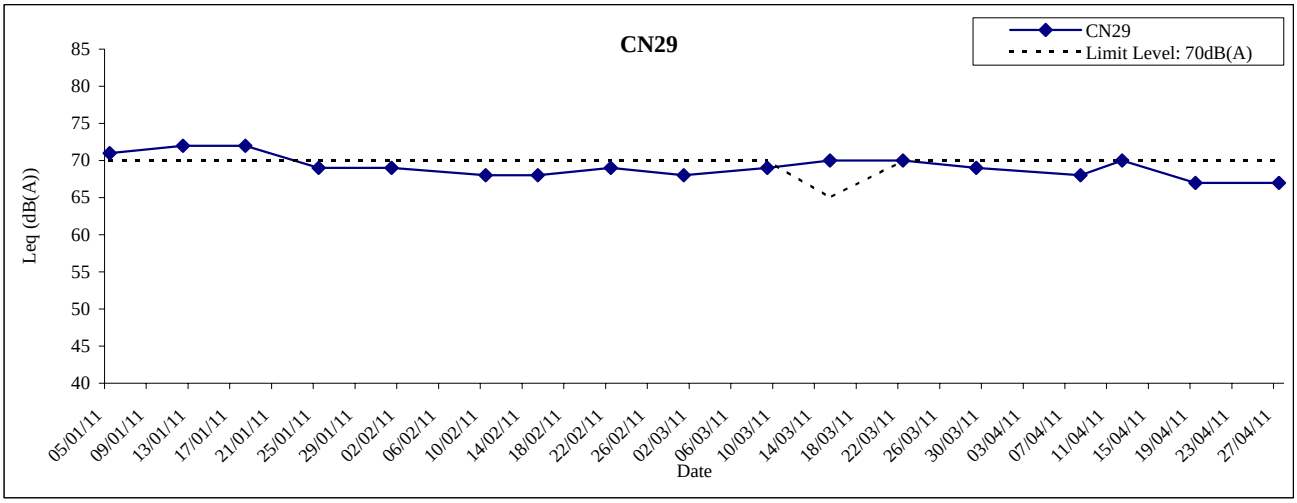


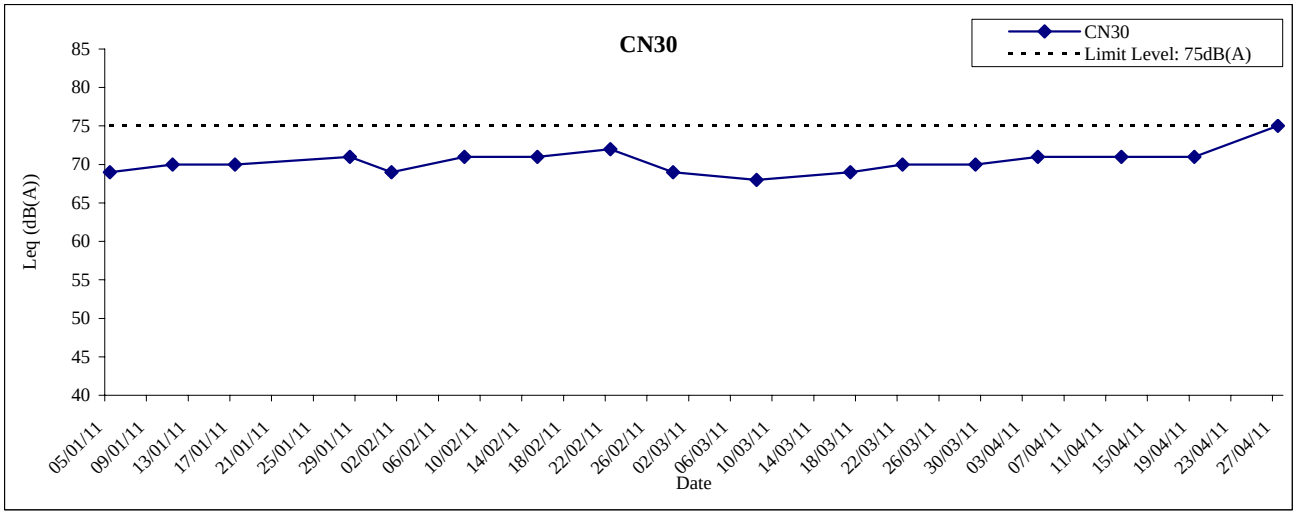


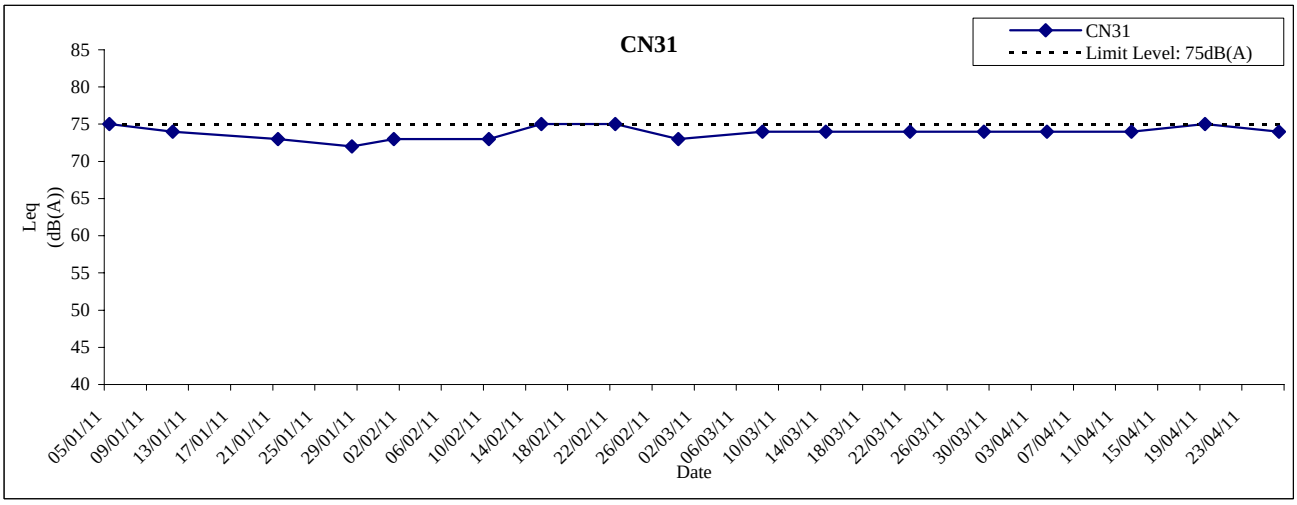


Remarks:
Noise limit level of CN29, which is school, is 70dB(A) on normal weekdays and 65dB(A) during examination period.

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN29, CN30 and CN31**	**Date**	**2011**
		APPENDIX	**F**

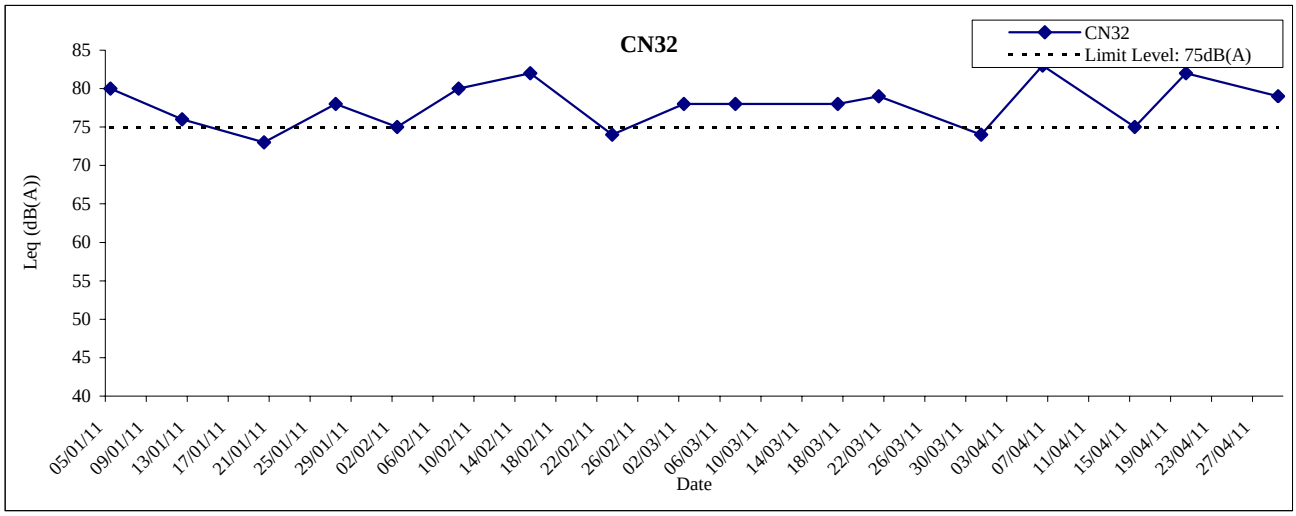

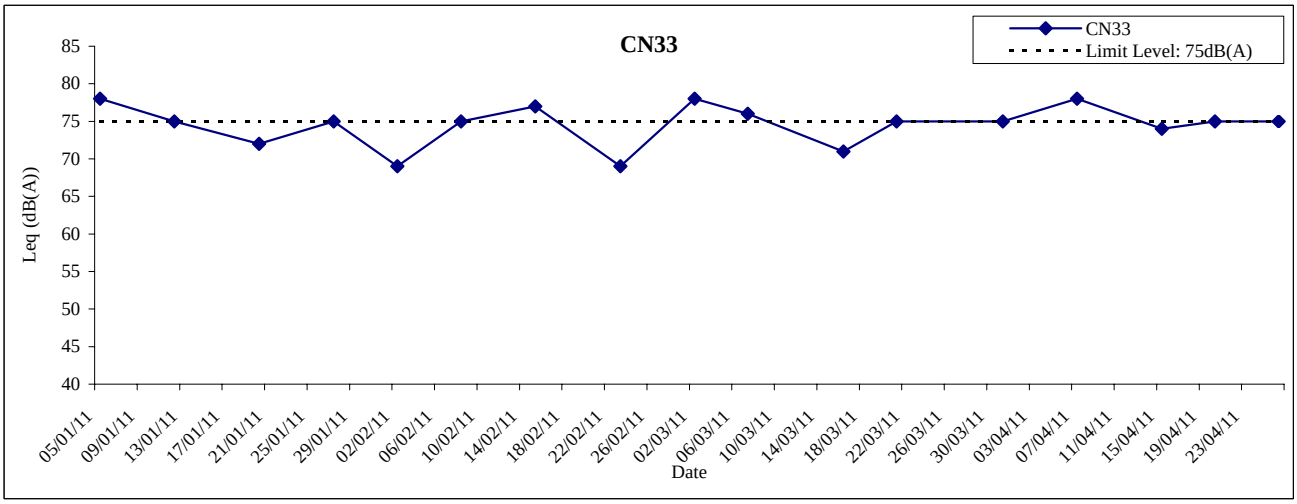

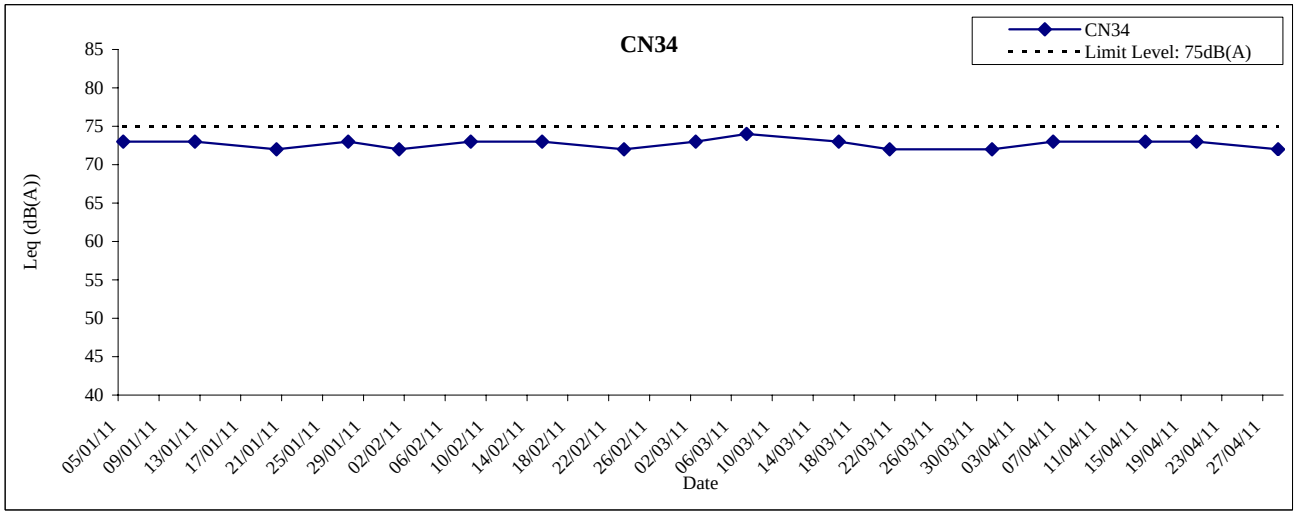

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of Noise** **Monitoring Results for Location CN32, CN33 and CN34**	**Date**	**2011**
		APPENDIX	**F**

APPENDIX F: Air Quality Monitoring Results - 24-hour TSP Monitoring

- AM1

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
02-Apr-11	65.9	217.3	260.0
08-Apr-11	99.5	217.3	260.0
14-Apr-11	117.7	217.3	260.0
20-Apr-11	185.6	217.3	260.0
26-Apr-11	202.5	217.3	260.0
29-Apr-11	94.3	217.3	260.0

- AM2

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
02-Apr-11	74.5	179.4	260.0
08-Apr-11	70.2	179.4	260.0
14-Apr-11	75.7	179.4	260.0
20-Apr-11	174.8	179.4	260.0
26-Apr-11	75.4	179.4	260.0
29-Apr-11	109.0	179.4	260.0

- AM3

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
04-Apr-11	**192.0**	154.7	260.0
09-Apr-11	127.6	154.7	260.0
15-Apr-11	108.5	154.7	260.0
20-Apr-11	76.7	154.7	260.0
26-Apr-11	102.0	154.7	260.0
30-Apr-11	113.4	154.7	260.0

- AM4

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
02-Apr-11	111.3	148.6	260.0
08-Apr-11	78.1	148.6	260.0
14-Apr-11	53.9	148.6	260.0
20-Apr-11	91.9	148.6	260.0
26-Apr-11	62.6	148.6	260.0
29-Apr-11	**174.5**	148.6	260.0

- AM5

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
04-Apr-11	93.7	152.0	260.0
09-Apr-11	68.7	152.0	260.0
15-Apr-11	83.0	152.0	260.0
20-Apr-11	74.9	152.0	260.0
26-Apr-11	50.7	152.0	260.0
30-Apr-11	98.8	152.0	260.0

- AM6

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
04-Apr-11	98.1	145.6	260.0
09-Apr-11	62.6	145.6	260.0
15-Apr-11	93.6	145.6	260.0
20-Apr-11	90.0	145.6	260.0
26-Apr-11	90.1	145.6	260.0
30-Apr-11	86.3	145.6	260.0

- AM7

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
04-Apr-11	61.4	149.8	260.0
09-Apr-11	54.0	149.8	260.0
15-Apr-11	96.6	149.8	260.0
20-Apr-11	66.9	149.8	260.0
26-Apr-11	61.9	149.8	260.0
30-Apr-11	121.2	149.8	260.0

- AM8

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
04-Apr-11	131.2	158.2	260.0
09-Apr-11	117.2	158.2	260.0
15-Apr-11	96.8	158.2	260.0
20-Apr-11	104.5	158.2	260.0
26-Apr-11	124.3	158.2	260.0
30-Apr-11	90.3	158.2	260.0

Remark: - Bold value indicated an Action level exceedance
- Bold & Italic value indicated an Limit level exceedance

APPENDIX F: Air Quality Monitoring Results - 24-hour TSP Monitoring

- AM9

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
02-Apr-11	140.4	171.2	260.0
08-Apr-11	89.2	171.2	260.0
14-Apr-11	113.6	171.2	260.0
20-Apr-11	144.1	171.2	260.0
26-Apr-11	75.3	171.2	260.0
29-Apr-11	69.7	171.2	260.0

- AM10

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
02-Apr-11	76.3	174.8	260.0
08-Apr-11	46.3	174.8	260.0
14-Apr-11	81.8	174.8	260.0
20-Apr-11	134.0	174.8	260.0
26-Apr-11	79.4	174.8	260.0
29-Apr-11	89.8	174.8	260.0

- AM11

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	89.5	160.3	260.0
06-Apr-11	86.3	160.3	260.0
11-Apr-11	126.3	160.3	260.0
16-Apr-11	73.1	160.3	260.0
21-Apr-11	64.1	160.3	260.0
27-Apr-11	116.9	160.3	260.0

- AM12

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	161.4	162.5	260.0
06-Apr-11	132.0	162.5	260.0
11-Apr-11	80.0	162.5	260.0
16-Apr-11	79.3	162.5	260.0
21-Apr-11	75.0	162.5	260.0
27-Apr-11	149.5	162.5	260.0

- AM13

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	172.5	180.3	260.0
06-Apr-11	147.7	180.3	260.0
11-Apr-11	95.3	180.3	260.0
16-Apr-11	86.2	180.3	260.0
21-Apr-11	71.5	180.3	260.0
27-Apr-11	162.4	180.3	260.0

- AM14

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	157.1	158.2	260.0
06-Apr-11	119.9	158.2	260.0
11-Apr-11	88.4	158.2	260.0
16-Apr-11	90.4	158.2	260.0
21-Apr-11	66.6	158.2	260.0
27-Apr-11	63.6	158.2	260.0

- AM15

Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	**226.7**	168.8	260.0
06-Apr-11	132.4	168.8	260.0
11-Apr-11	106.9	168.8	260.0
16-Apr-11	87.4	168.8	260.0
21-Apr-11	73.3	168.8	260.0
27-Apr-11	78.5	168.8	260.0


- AM16


Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	150.7	155.9	260.0
06-Apr-11	90.3	155.9	260.0
11-Apr-11	126.4	155.9	260.0
16-Apr-11	95.8	155.9	260.0
21-Apr-11	154.6	155.9	260.0
27-Apr-11	86.4	155.9	260.0

- AM17


Date	24-hour TSP Monitoring Results	Action Level	Limit Level
	(μg/m^3)	(μg/m^3)	(μg/m^3)
01-Apr-11	**213.6**	179.3	260.0
06-Apr-11	158.4	179.3	260.0
12-Apr-11	151.3	179.3	260.0
16-Apr-11	116.1	179.3	260.0
21-Apr-11	87.1	179.3	260.0
27-Apr-11	80.1	179.3	260.0


Remark: Bold value indicated an Action level exceedance
Bold & Italic value indicated an Limit level exceedance

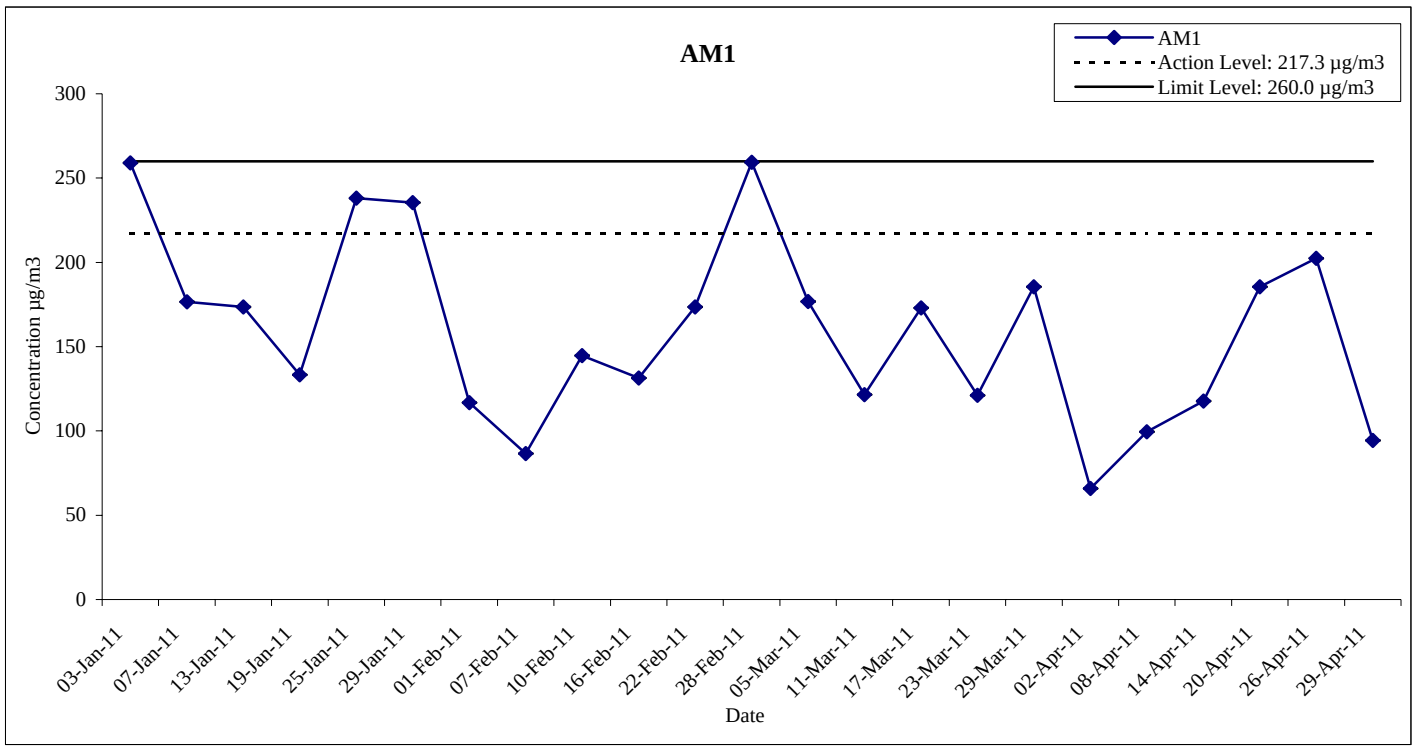

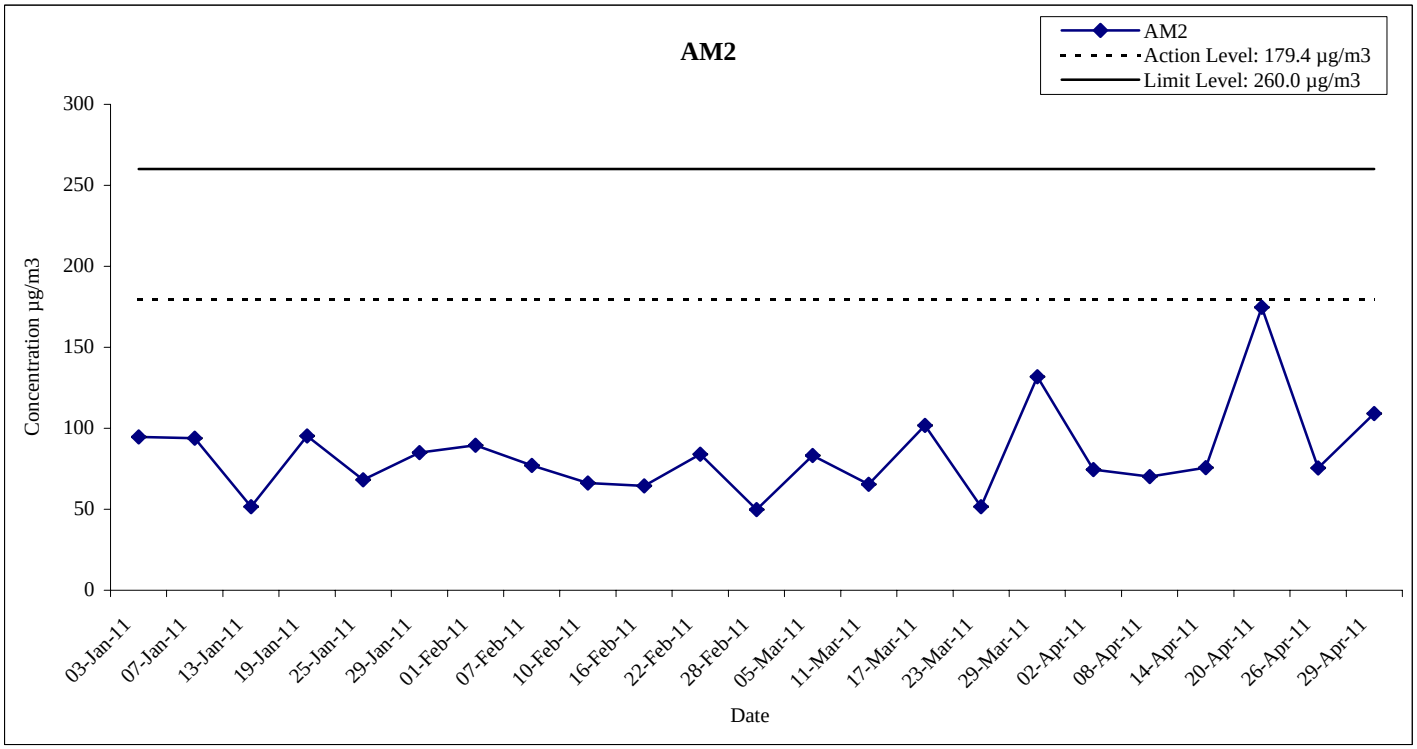



MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM1 and AM2**	**Date**	**2011**
		APPENDIX	**F**

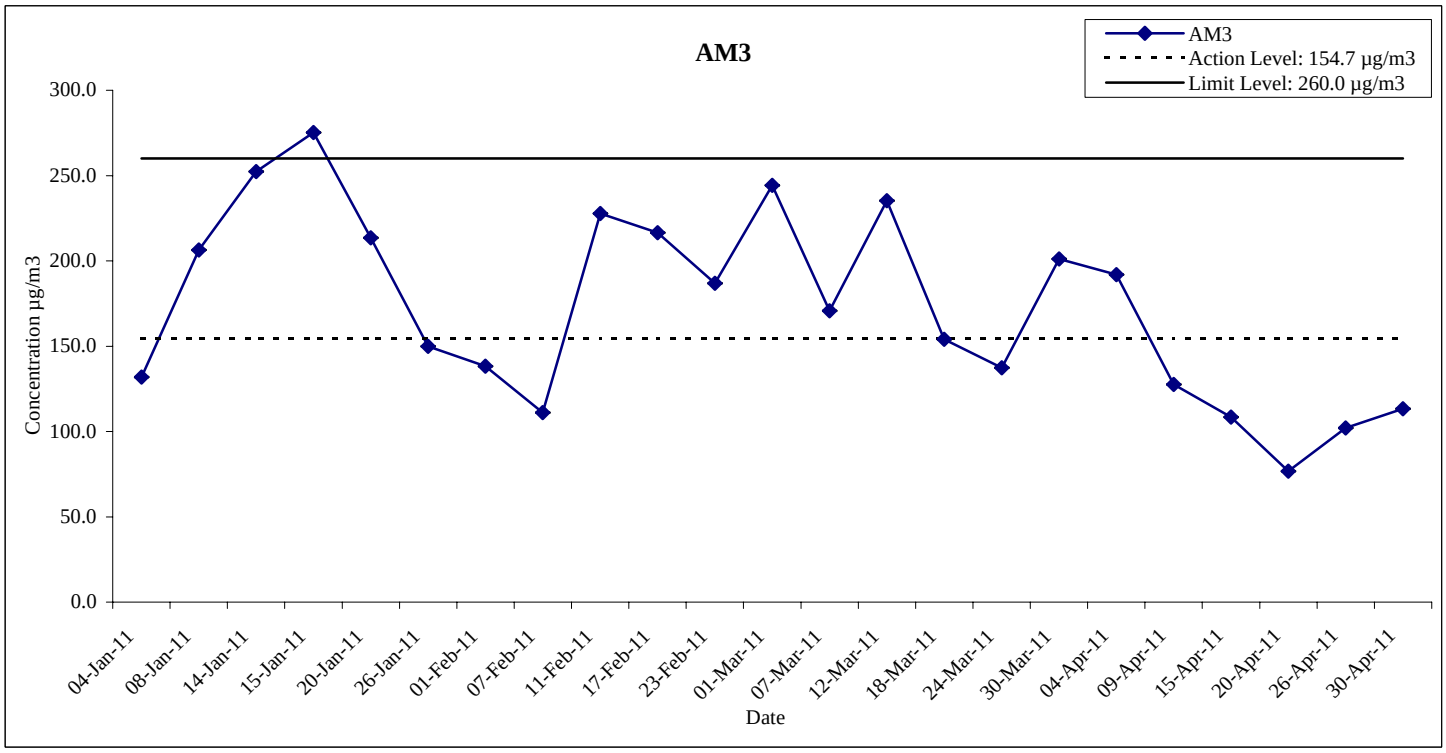

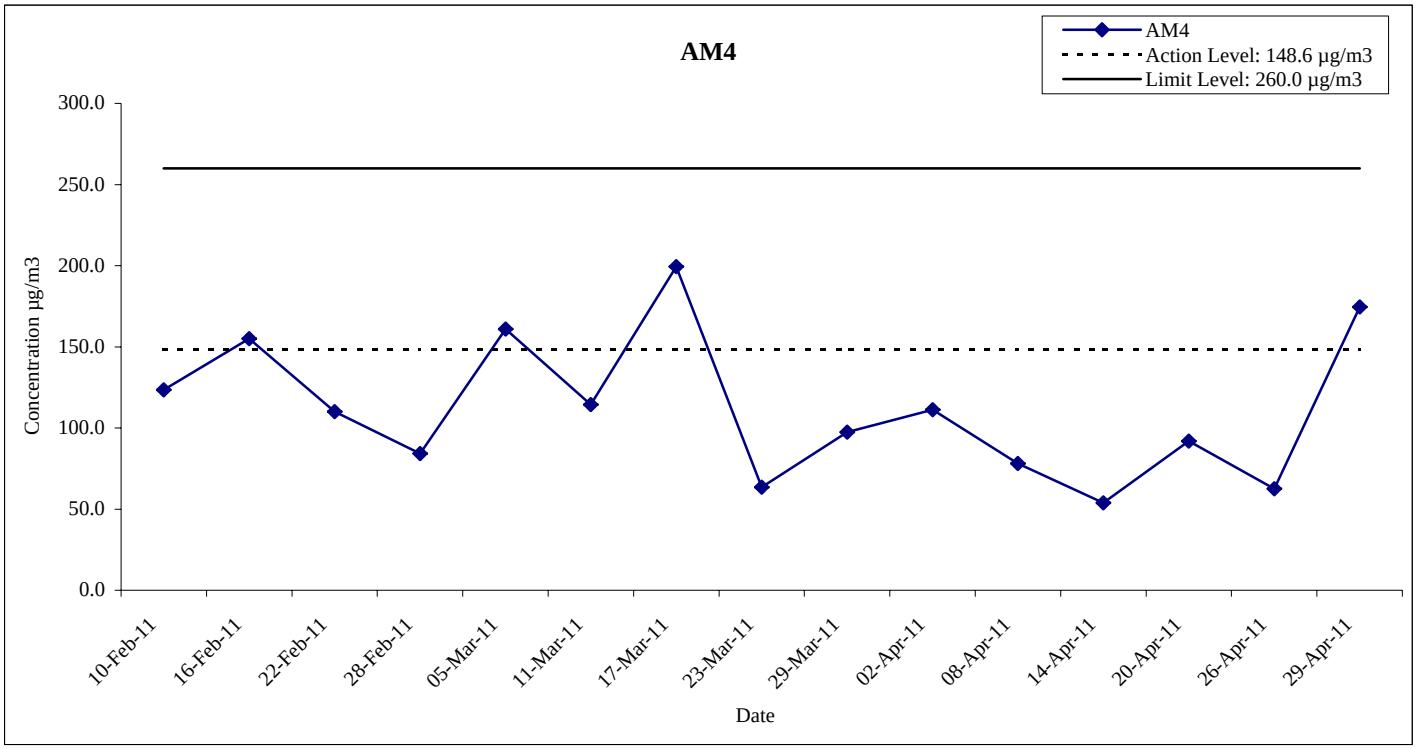



MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM3 and AM4**	**Date**	**2011**
		APPENDIX	**F**

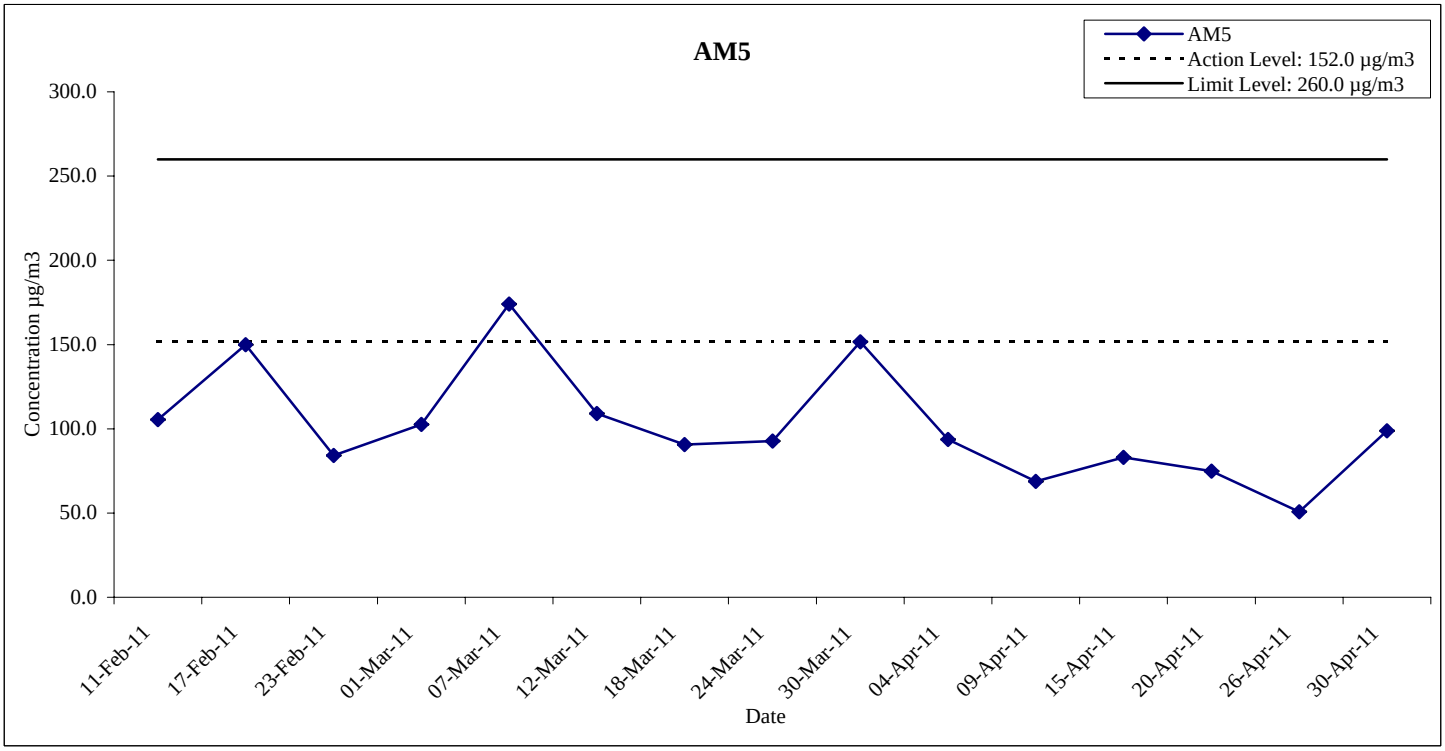

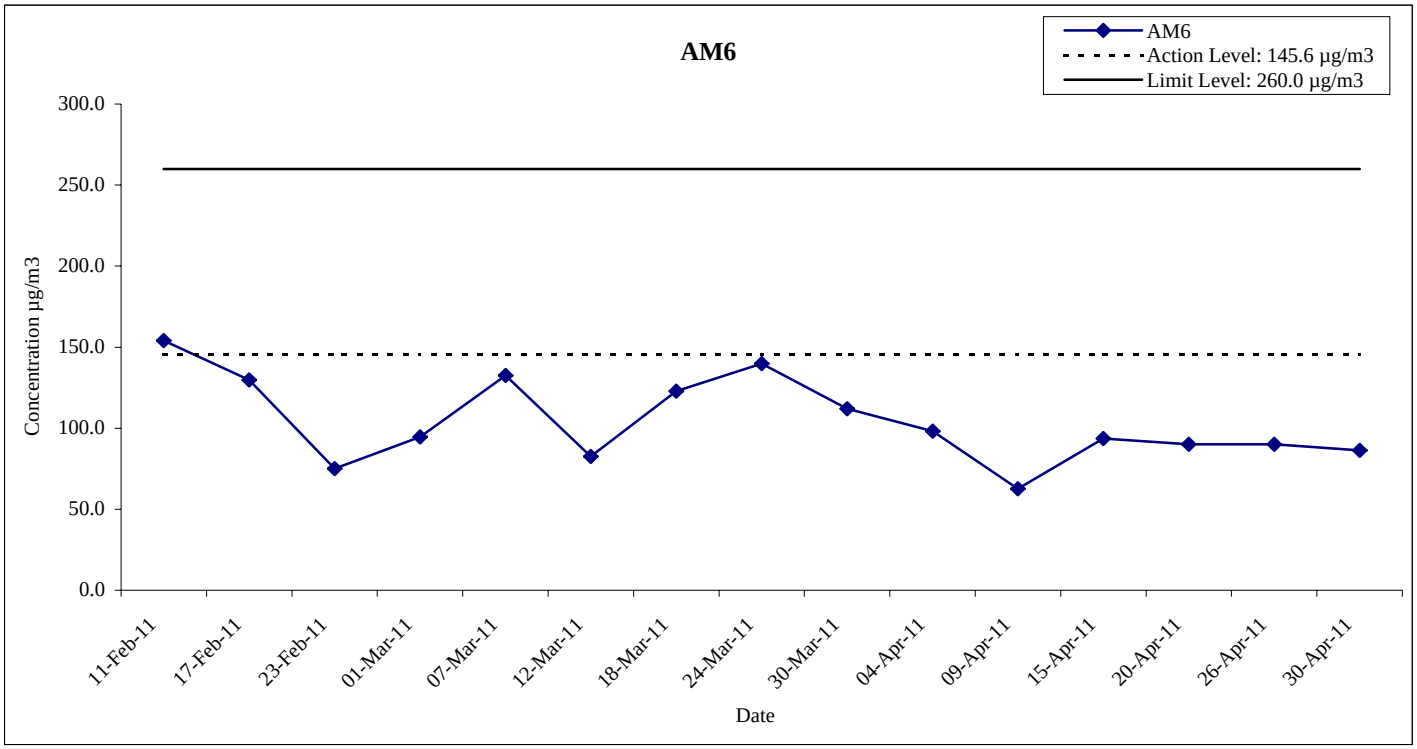


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM5 and AM6**	**Date**	**2011**
		APPENDIX	**F**

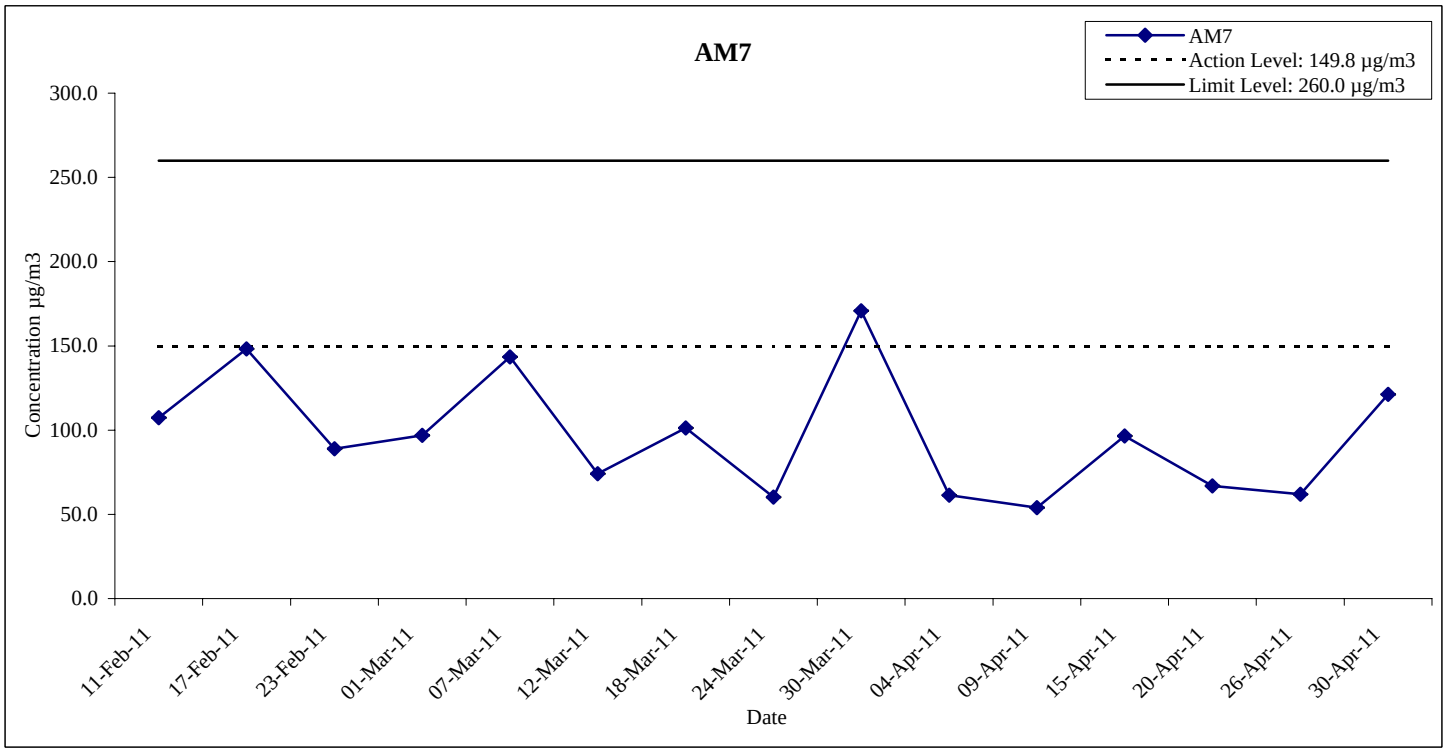


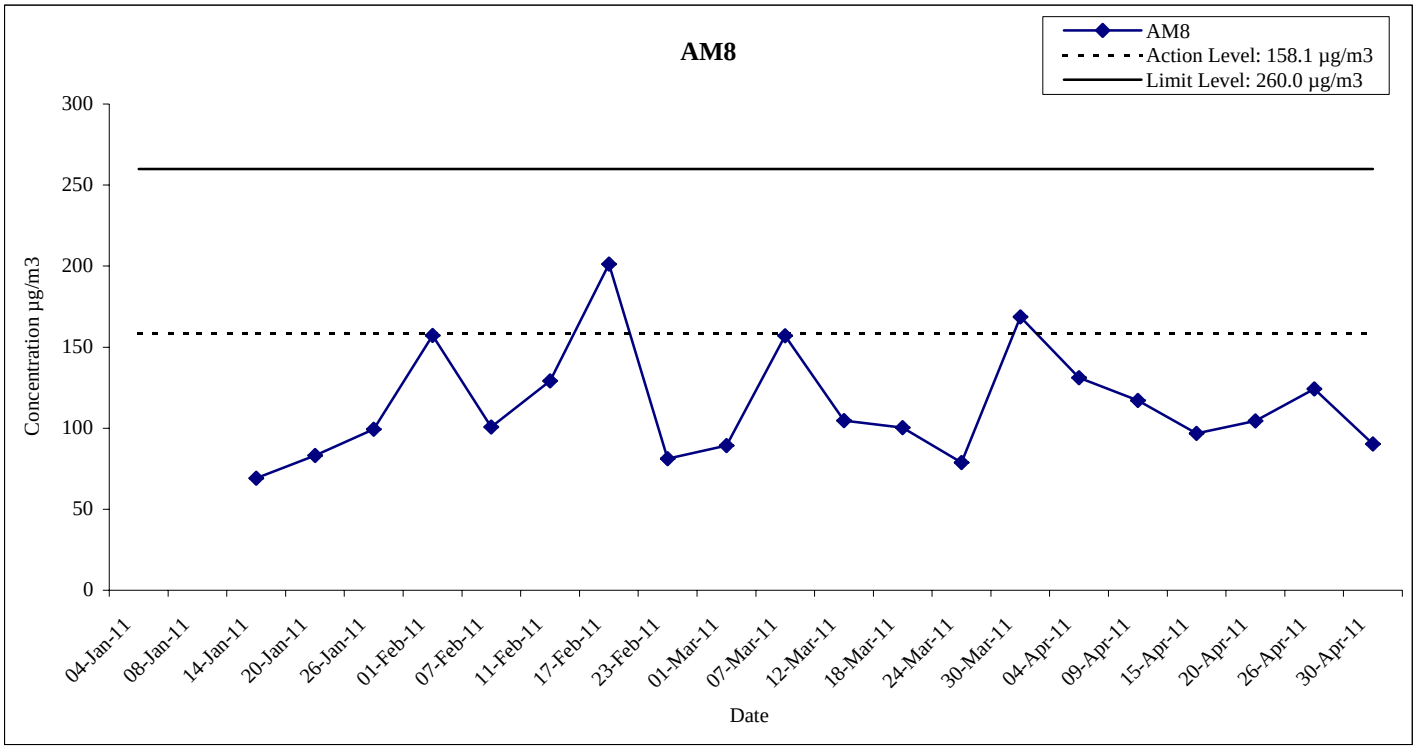


Remarks:
Impact monitoring for AM8 was suspended on 4 and 8 January 2011 due to the termination of power supply by original house owner and it was resumed on 14 January 2011.


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM7 and AM8**	**Date**	**2011**
		APPENDIX	**F**

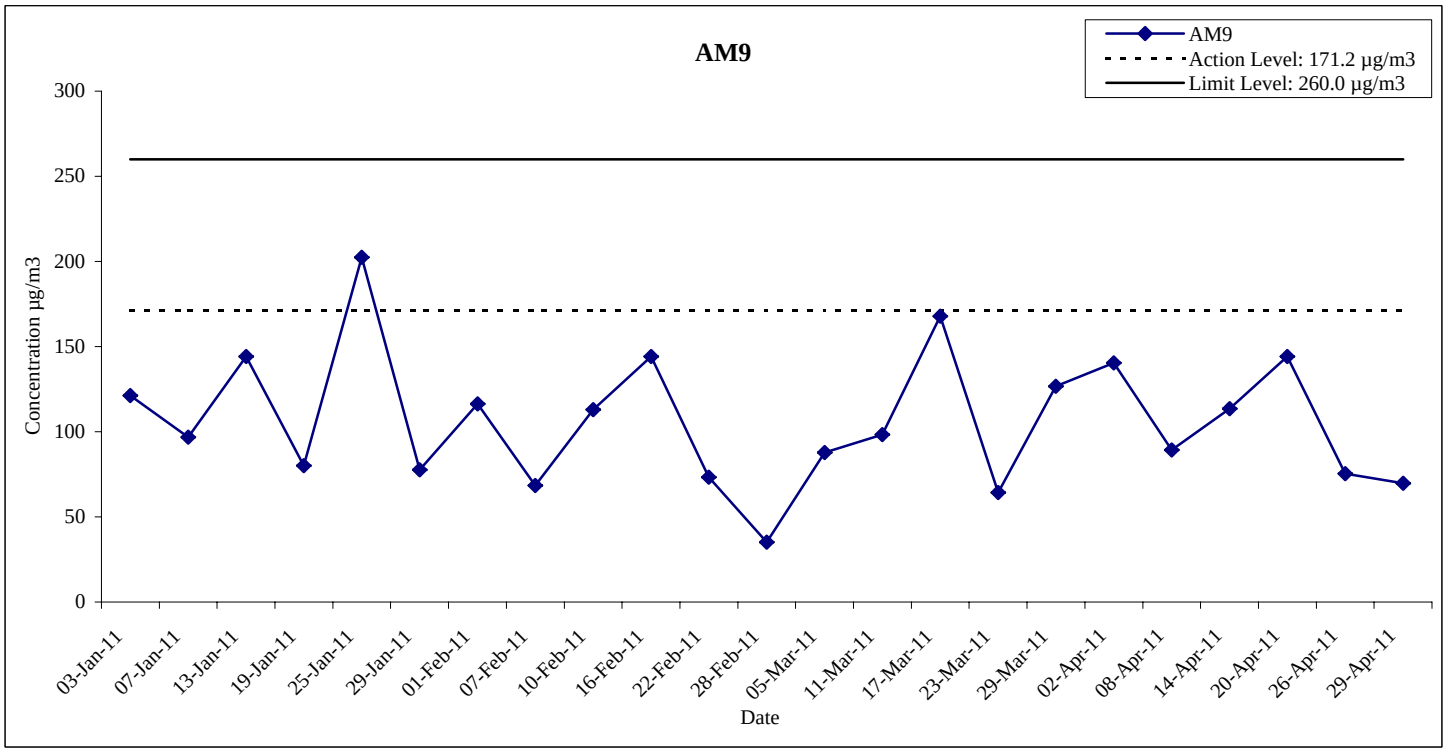

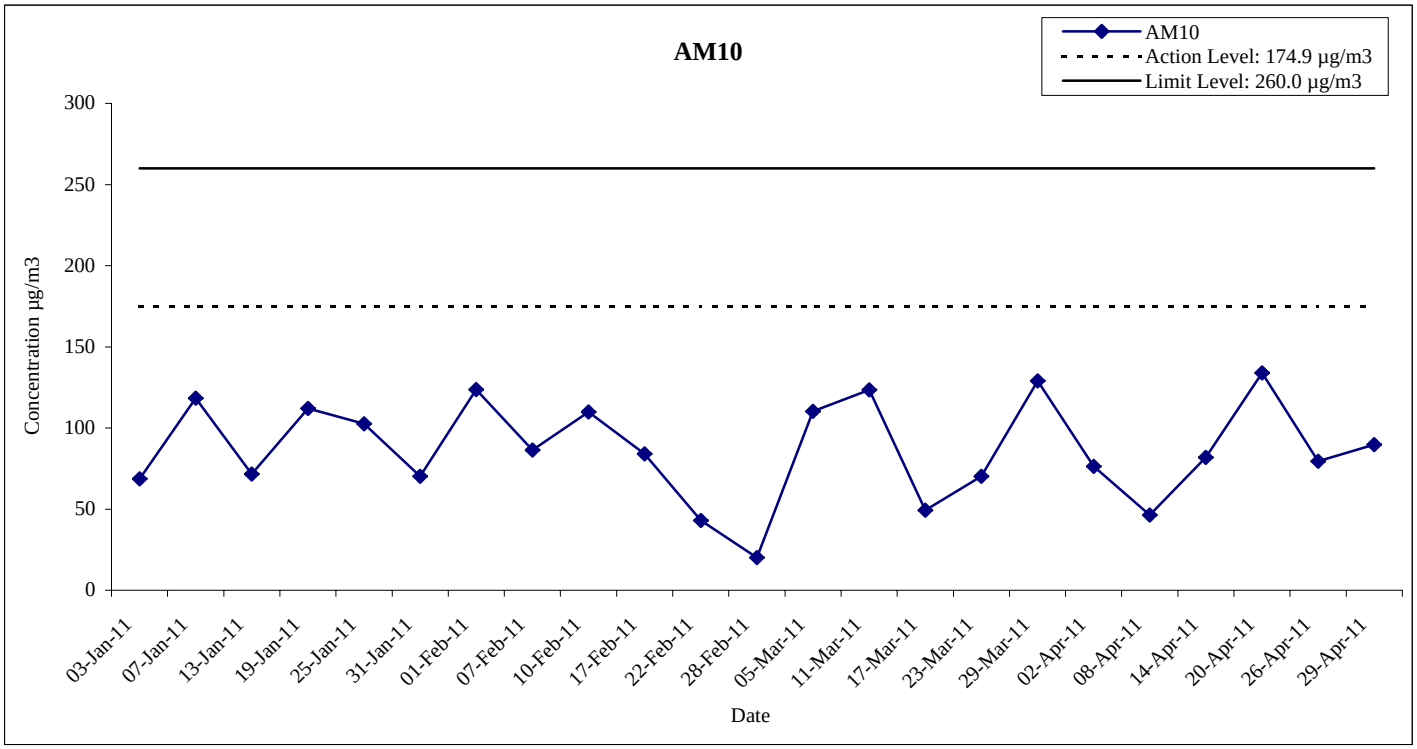



MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM9 and AM10**	**Date**	**2011**
		APPENDIX	**F**

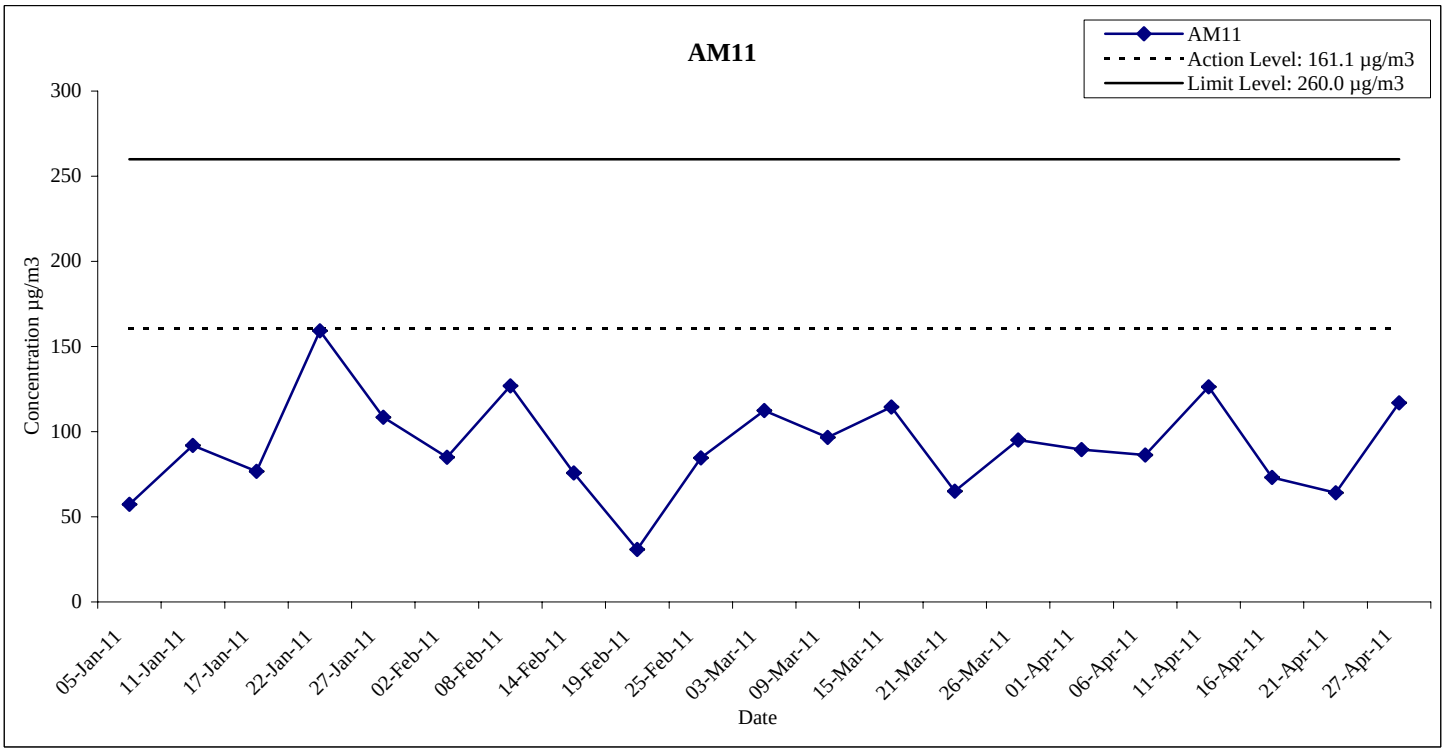

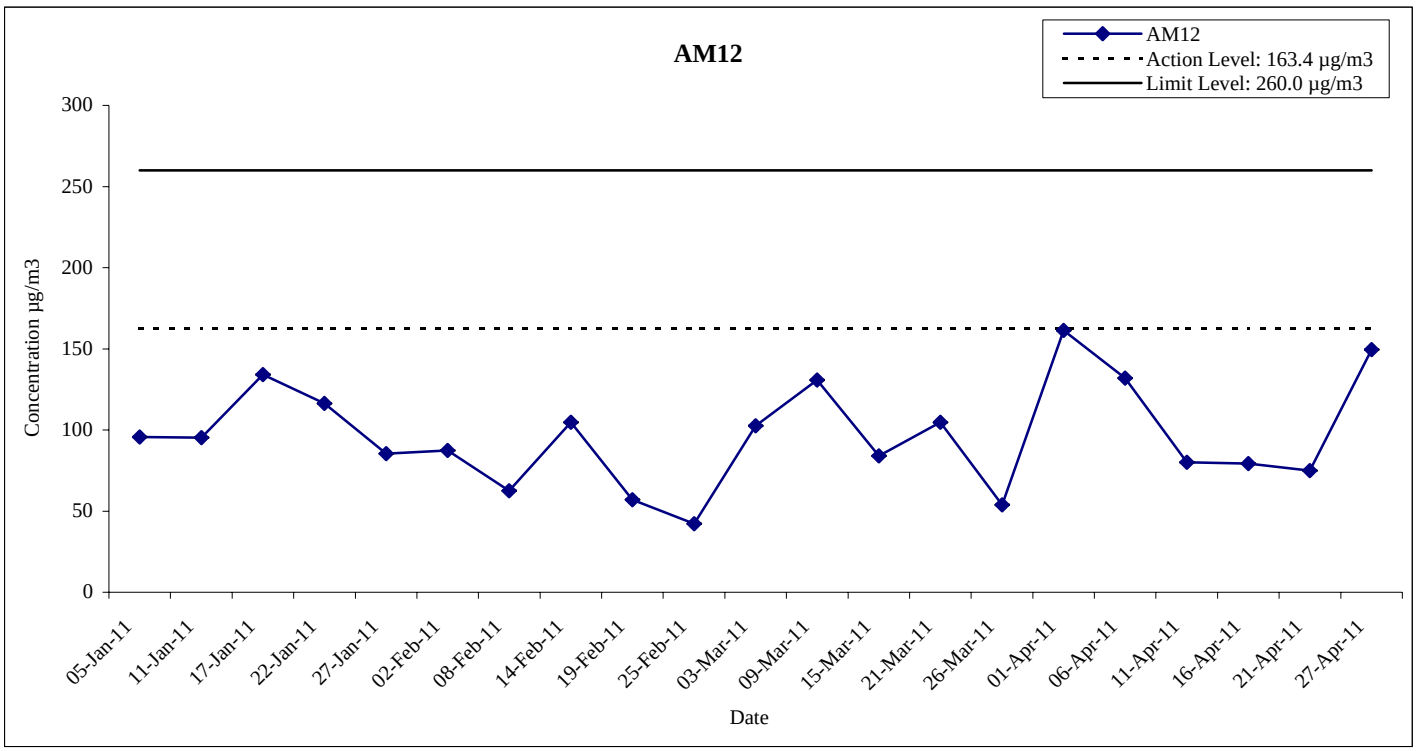



MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM11 and AM12**	**Date**	**2011**
		APPENDIX	**F**

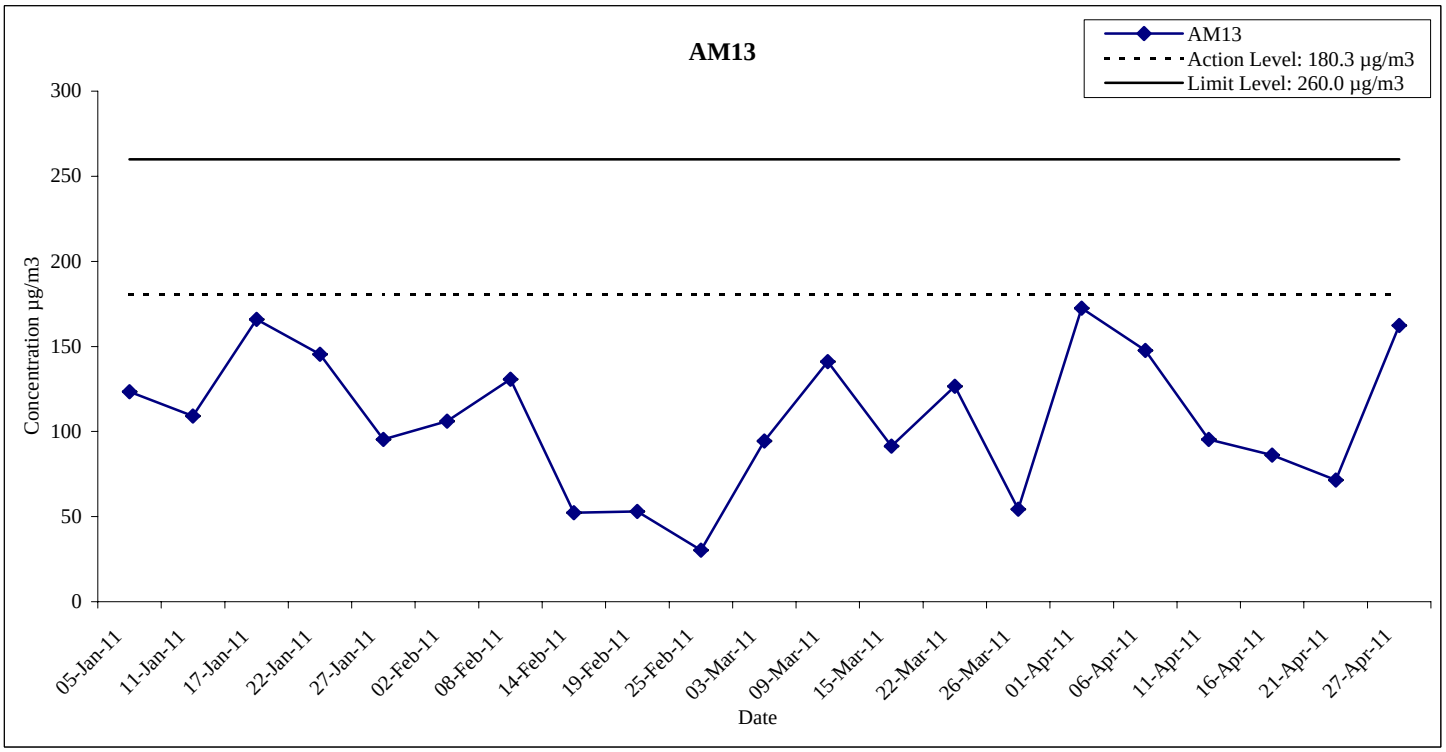

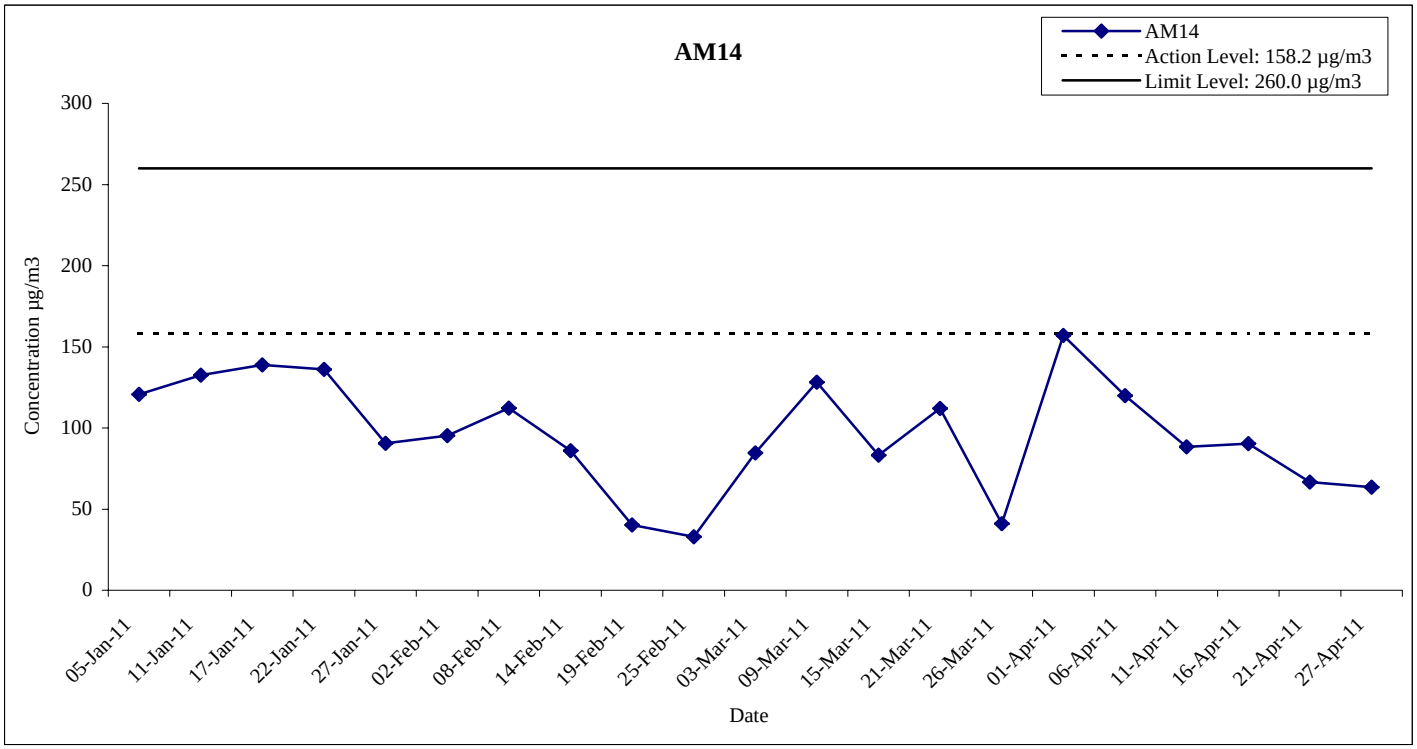


MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM13 and AM14**	**Date**	**2011**
		APPENDIX	**F**

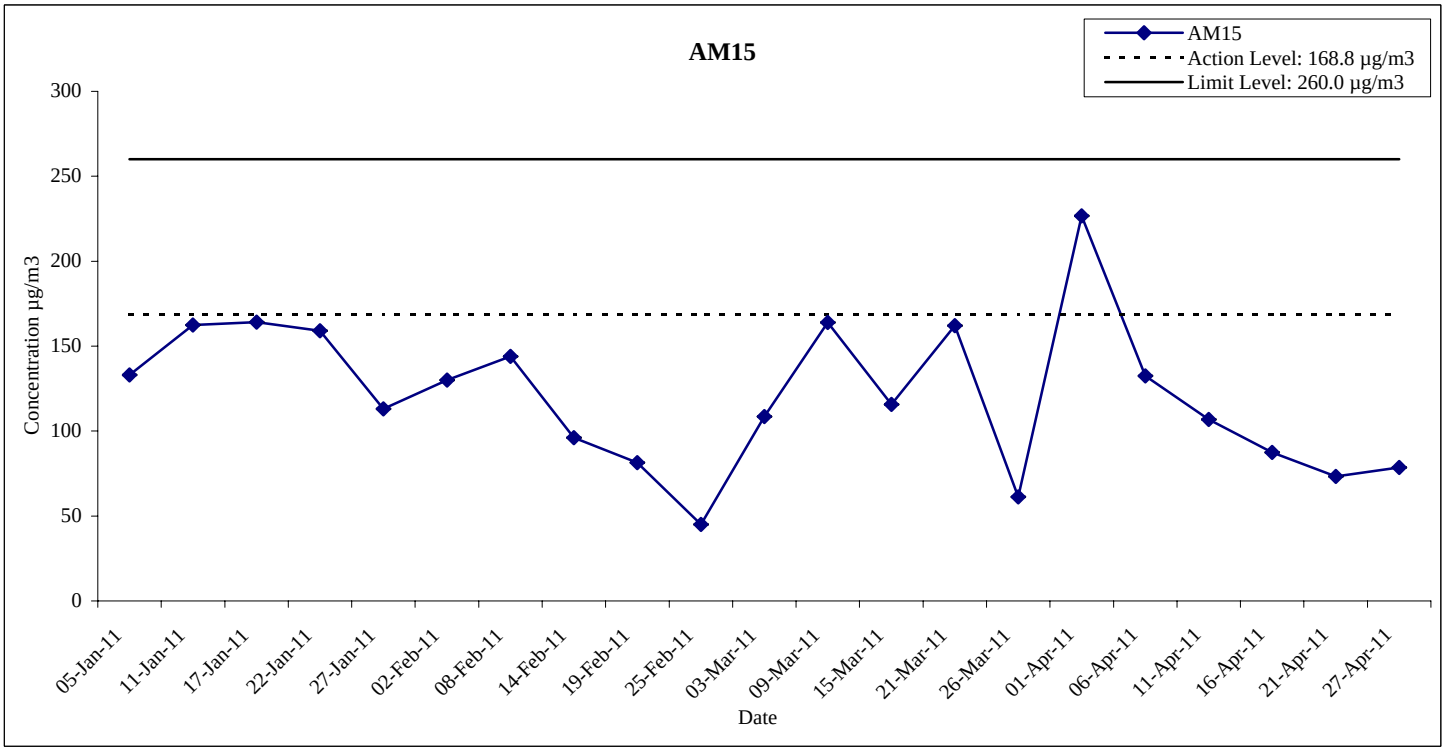

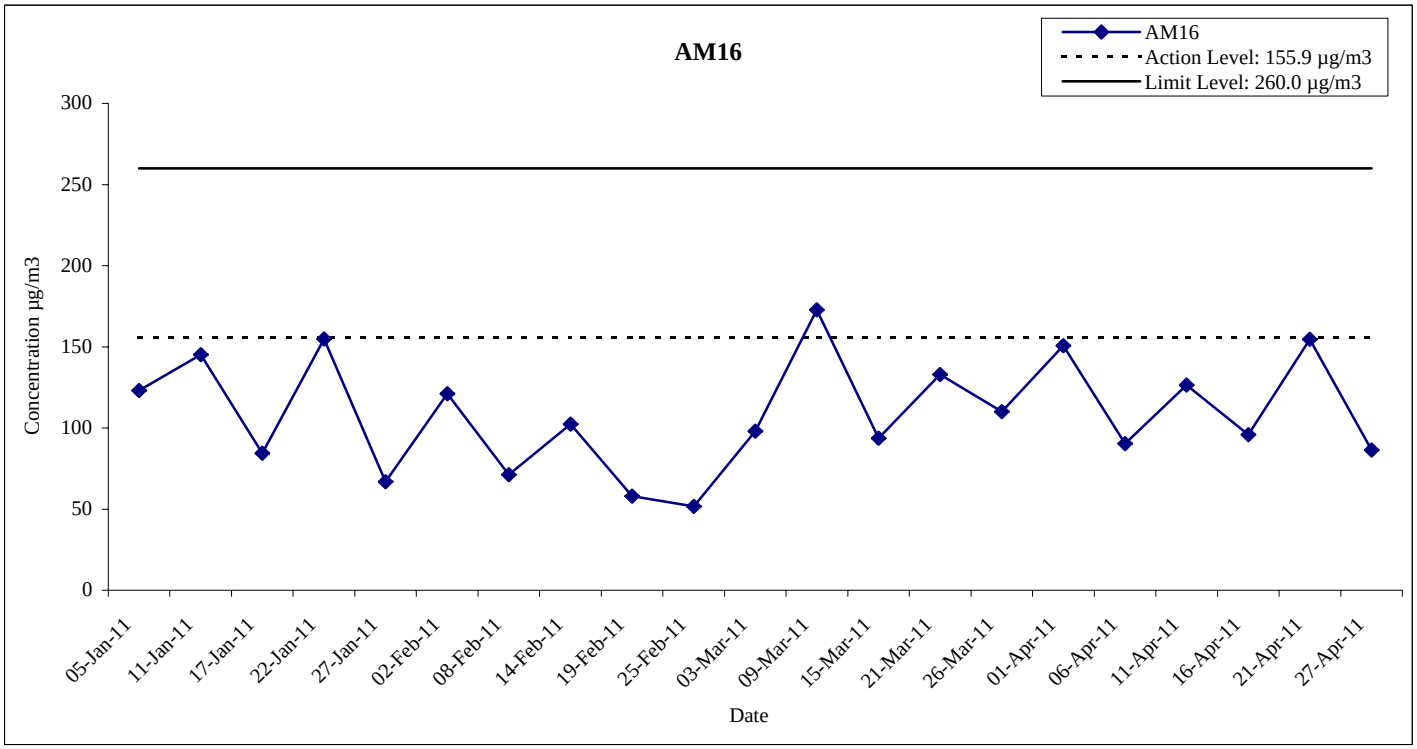

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Results for Location AM15 and AM16**	**Date**	**2011**
		APPENDIX	**F**

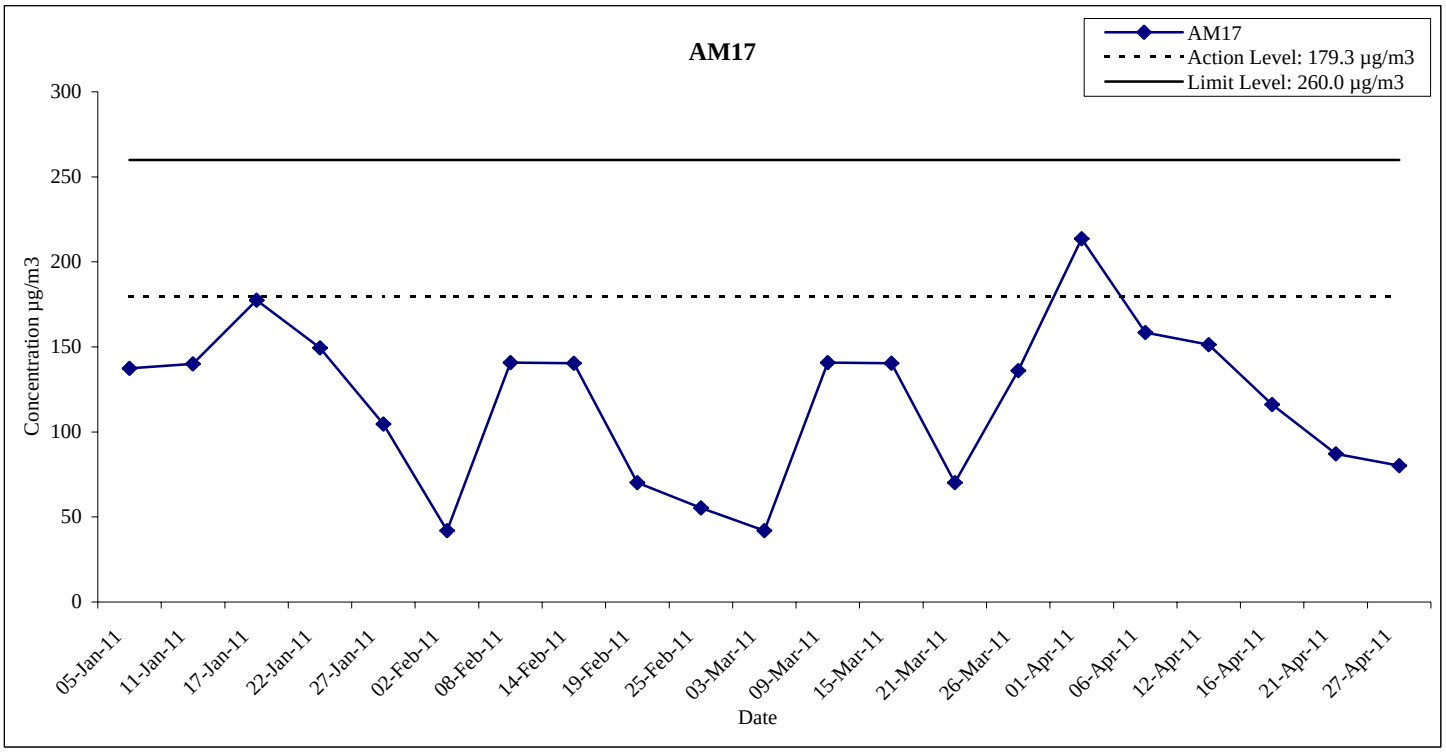

MTR	Hong Kong Section of Guangzhou-Shenzhen-Hong Kong Express Rail Link **Graphical Presentation of 24-hour TSP** **Monitoring Result for Location AM17**	**Date**	**2011**
		APPENDIX	**F**

Appendix G

Bird Species and Abundance Recorded during Avifauna Survey

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: MPV
Survey Site: MPV-1
Survey Date: 12 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location												Sub-total	Walk Transect
			MPV-1/P1	MPV-1/P2	MPV-1/P3	MPV-1/P4	MPV-1/P5	MPV-1/P6	MPV-1/P7	MPV-1/P8	MPV-1/P9	MPV-1/P10	MPV-1/P11	MPV-1/P12		
Little Grebe	小鸊鹈	P	3												3	
Great Egret	大白鷺	P		1		1									2	
Intermediate Egret	中白鷺	M,P								1					1	
Little Egret	小白鷺	P	3		7		2	8		7		3			30	√
Cattle Egret	牛背鷺	P					1								1	√
Chinese Pond Heron	池鷺	P	2	1	2		5		1	3		1			15	√
Black-crowned Night Heron	夜鷺	P												1	1	
Osprey	鶚(魚鷹)	W										1			1	
Black Kite	黑鳶(麻鷹)	W,R										1			1	√
White-breasted Waterhen	白胸苦惡鳥	R													0	√
Common Sandpiper	磯鷸	M,W			1		2	2	2	2	3				12	
Black-headed Gull	紅嘴鷗	W						1							1	
Spotted Dove	珠頸斑鳩	R	2	1		1	1	1	1	2	3	2	1		15	
Large Hawk Cuckoo	鷹鵑	Su													0	√
Common Koel	噪鵑	Su,R		1											1	√
Greater Coucal	褐翅鴉鵑	R			1										1	
Pied Kingfisher	斑魚狗	R										1	1		2	
Common Kingfisher	普通翠鳥	AM,P						1			1	1			3	
White-throated Kingfisher	白胸翡翠	AM,P													0	√
Barn Swallow	家燕	SpM,Su	2		23	6	6					1		2	40	
Yellow Wagtail	黃鶺鴒	M,W			2		1	2		2	1				8	
White Wagtail	白鶺鴒	W,R			4	1	1	4		1	2	1			14	
Olive-backed Pipit	樹鷚	W				2					1				3	
Red-throated Pipit	紅喉鷚	M,W			2		6								6	
Red-whiskered Bulbul	紅耳鵯	R								1		1			2	√
Chinese Bulbul	白頭鵯	R			1								1		2	√
Oriental Magpie Robin	鵲鴝	R	3												3	√
Masked Laughingthrush	黑臉噪鶥	R	1												1	√
Yellow-bellied Prinia	黃腹山鷦鶯	R			6				2	1		3		2	14	√
Plain Prinia	純色山鷦鶯	R			2		2		3	2		1			10	√
Common Tailorbird	長尾縫葉鶯	R											1		1	
Dusky Warbler	褐柳鶯	W	1		1										2	
Scaly-breasted Munia	斑文鳥	R										45			45	
Eurasian Tree Sparrow	麻雀	R					2	15							17	
Black-collared Starling	黑領椋鳥	R					1			1					2	√
Crested Myna	八哥	R			2		2			1	2				7	
Black Drongo	黑卷尾	M,Su		1											1	
Common Magpie	喜鵲	R				1								1	2	
Large-billed Crow	大嘴烏鴉	R													0	√
Collared Crow	白頸鴉	R									1				1	
Azure-winged Magpie	灰喜鵲	Category E*													0	√
No. of Birds at Each Point:			**17**	**5**	**54**	**12**	**32**	**34**	**9**	**24**	**14**	**62**	**4**	**6**		
No. of Birds Recorded from Point Count:			**273**													
No. of Species Recorded from Point Count:			**36**													
Total No. of Species:			**41**													
Total No. of Species of Conservation Interest:			**9**													

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; Su=summer visitor; M=migrant; A=autumn; Sp=spring; P=present all year; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al* . (2001): The Avifauna of Hong Kong]
* Category E: Species for which all published Hong Kong records are considered likely to relate to birds that have escaped or have been released from captivity and do not possess a Principal Status.

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: Access road leading to TPP
Survey Site: TPP-1
Survey Date: 12 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location					Sub-total	Walk Transect
			TPP-1/P1	TPP-1/P2	TPP-1/P3	TPP-1/P4	TPP-1/P5		
Little Egret	小白鷺	P			1			1	
Cattle Egret	牛背鷺	P	5					5	
Chinese Pond Heron	池鷺	P	1	1		1		3	
White-breasted Waterhen	白胸苦惡鳥	R	2	1	1			4	
Green Sandpiper	白腰草鷸	W		6	10			16	
Wood Sandpiper	林鷸	M,W	1	2	34			37	
Common Snipe	扇尾沙錐	W			2			2	
Spotted Dove	珠頸斑鳩	R	9	2		1	2	14	
Common Koel	噪鵑	Su, R			1			1	√
Large Hawk Cuckoo	鷹鵑	Su						0	√
Barn Swallow	家燕	SpM, Su	3	5	6	7		21	
Yellow Wagtail	黃鶺鴒	M,W		1	2	1		4	
Grey Wagtail	灰鶺鴒	W	1			1		2	
White Wagtail	白鶺鴒	W,R		2	4	3		9	
Olive-backed Pipit	樹鷚	W		2	1			3	
Red-throated Pipit	紅喉鷚	M,W		2				2	
Red-whiskered Bulbul	紅耳鵯	R	7		3		4	14	
Chinese Bulbul	白頭鵯	R			2	7		9	
Oriental Magpie Robin	鵲鴝	R	3	2	2	1	2	10	
Common Stonechat	黑喉石鴴	W,M				2		2	
Masked Laughingthrush	黑臉噪鶥	R	8			1		9	
Yellow-bellied Prinia	黃腹山鷦鶯	R	3	2	4	1		10	
Plain Prinia	純色山鷦鶯	R			2	1	1	4	
Dusky Warbler	褐柳鶯	W				1		1	
Japanese White-eye	暗綠繡眼鳥	R,?W	1					1	
Scaly-breasted Munia	斑文鳥	R				14		14	
Eurasian Tree Sparrow	麻雀	R				6	3	9	√
Black-collared Starling	黑領椋鳥	R	3	1	4	4		12	
White-shouldered Starling	灰背椋鳥	M,W,Su				8		8	
Crested Myna	八哥	R			2	4		6	
Large-billed Crow	大嘴烏鴉	R		2				2	√
No. of Birds at Each Point:			**47**	**31**	**81**	**64**	**12**		
No. of Birds Recorded from Point Count:			**235**						
No. of Species Recorded from Point Count:			**30**						
Total No. of Species:			**31**						
Total No. of Species of Conservation Interest:			**4**						

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; M=migrant; P=present all year; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al*. (2001): The Avifauna of Hong Kong]

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: Access road leading to TPP
Survey Site: TPP-2
Survey Date: 12 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location				Sub-total	Walk Transect
			TPP-2/P1	TPP-2/P2	TPP-2/P3	TPP-2/P4		
Little Egret	小白鷺	P					0	√
Little Ringed Plover	金眶鴴(黑領鴴)	W,R			1		1	
Green Sandpiper	白腰草鷸	W			1		1	
Wood Sandpiper	林鷸	M,W			1		1	
Common Sandpiper	磯鷸	M,W			2		2	
Spotted Dove	珠頸斑鳩	R	2	1			3	
Large Hawk Cuckoo	鷹鵑	Su					0	√
Plaintive Cuckoo	八聲杜鵑	Su					0	√
Common Koel	噪鵑	Su,R					0	√
Barn Swallow	家燕	SpM,Su			12		12	√
Grey Wagtail	灰鶺鴒	W	1				1	
White Wagtail	白鶺鴒	W,R	1	3	1		5	
Red-whiskered Bulbul	紅耳鵯	R			2		2	√
Chinese Bulbul	白頭鵯	R			1		1	√
Oriental Magpie Robin	鵲鴝	R	2	1			3	√
Yellow-bellied Prinia	黃腹山鷦鶯	R	1				1	√
Plain Prinia	純色山鷦鶯	R					0	√
Japanese White-eye	暗綠繡眼鳥	R,?W		6			6	
Eurasian Tree Sparrow	麻雀	R		6			6	√
Black-collared Starling	黑領椋鳥	R		2			2	
Common Myna	家八哥	R	1				1	
No. of Birds at Each Point:			**8**	**19**	**21**	**0**		
No. of Birds Recorded from Point Count:			**48**					
No. of Species Recorded from Point Count:			**16**					
Total No. of Species:			**21**					
Total No. of Species of Conservation Interest:			**2**					

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; Su=summer visitor; M=migrant; Sp=spring; P=present all year
[Principal status was assessed with reference to Carey *et al*. (2001): The Avifauna of Hong Kong]

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: Access road leading to TPP
Survey Site: TPP-3
Survey Date: 12 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location			Sub-total
			TPP-3/P1	TPP-3/P2	TPP-3/P3	
Greater Coucal	褐翅鴉鵑	R		1		1
Red-whiskered Bulbul	紅耳鵯	R		6	3	9
Chinese Bulbul	白頭鵯	R		2	2	4
Masked Laughingthrush	黑臉噪鶥	R			3	3
Yellow-bellied Prinia	黃腹山鷦鶯	R		3	2	5
Plain Prinia	純色山鷦鶯	R		1		1
Black Drongo	黑卷尾	M,Su			2	2
No. of Birds at Each Point:			**0**	**13**	**12**	
No. of Birds Recorded from Point Count:			**25**			
No. of Species Recorded from Point Count:			**7**			
Total No. of Species:			**7**			
Total No. of Species of Conservation Interest:			**0**			

Note:

(1) Species in bold represents Species of Conservation Interest.

(2) R=resident; W=winter visitor; Su=summer visitor; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al* . (2001): The Avifauna of Hong Kong]

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: SSS / ERS
Survey Site: SSS-2a
Survey Date: 12 April 2011

Common Name (1)	Chinese Name	Principal Status (2)	SSS-2a/P1	SSS-2a/P3	Sub-total
Black Kite	黑鳶(麻鷹)	W,R	1		1
White-breasted Waterhen	白胸苦惡鳥	R		1	1
Red-whiskered Bulbul	紅耳鵯	R	1	1	2
Chinese Bulbul	白頭鵯	R	2	1	3
Oriental Magpie Robin	鵲鴝	R		2	2
Yellow-bellied Prinia	黃腹山鶯	R	1		1
Common Tailorbird	長尾縫葉鶯	R	1		1
Japanese White-eye	暗綠繡眼鳥	R,?W		1	1
Eurasian Tree Sparrow	麻雀	R	5		5
		No. of Birds at Each Point:	**10**	**6**	
		No. of Birds Recorded from Point Count:	**16**		
		No. of Species Recorded from Point Count:	**9**		
		Total No. of Species:	**9**		
		Total No. of Species of Conservation Interest:	**0**		

Note:

(1) Species in bold represents Species of Conservation Interest.

(2) R=resident; W=winter visitor; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al*. (2001): The Avifauna of Hong Kong]

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: SSS / ERS
Survey Site: SSS-3
Survey Date: 19 April 2011

Common Name (1)	Chinese Name	Principal Status (2)	Point Count Location												Sub-total	Walk Transect
			SSS-3/P1	SSS-3/P2	SSS-3/P3	SSS-3/P4	SSS-3/P5	SSS-3/P6	SSS-3/P7	SSS-3/P8	SSS-3/P9	SSS-3/P10	SSS-3/P11	SSS-3/P12		
Cattle Egret	牛背鷺	P											2	2	4	
Chinese Pond Heron	池鷺	P						1	2		5		3	1	12	√
Crested Serpent Eagle	蛇鵰	R,M													0	√
White-breasted Waterhen	白胸苦惡鳥	R						1	1	1			1		4	√
Rock Dove	原鴿	R											1		1	
Spotted Dove	珠頸斑鳩	R	2	1			1	1			2	6	1		14	√
Rose-ringed Parakeet	紅領綠鸚鵡	R							1						1	
Large Hawk Cuckoo	鷹鵑	Su			1										1	
Common Koel	噪鵑	Su,R			1	1	1		1					1	5	√
Greater Coucal	褐翅鴉鵑	R							1				2	1	4	√
Barn Swallow	家燕	SpM,Su	2				1	2	1		2	2	5	1	16	√
Yellow Wagtail	黃鶺鴒	M,W			1							3			4	√
Grey Wagtail	灰鶺鴒	W													0	√
White Wagtail	白鶺鴒	W,R	1						1				1		3	
Olive-backed Pipit	樹鷚	W												2	2	√
Red-whiskered Bulbul	紅耳鵯	R		1	1			1	5	3	6		3		20	√
Chinese Bulbul	白頭鵯	R		1			1				6		1		9	√
Oriental Magpie Robin	鵲鴝	R		1	1			1	2		2		1		8	√
Common Stonechat	黑喉石鴴	W,M										1		1	2	√
Blue Whistling Thrush	紫嘯鶇	R	1												1	
Masked Laughingthrush	黑臉噪鶥	R		1			1		3		1			1	7	√
Yellow-bellied Prinia	黃腹山鷦鶯	R	1	2	1			2	4	2	1	1	2	3	19	√
Plain Prinia	純色山鷦鶯	R							1			2	2		5	
Common Tailorbird	長尾縫葉鶯	R	1			1			1					1	4	√
Dusky Warbler	褐柳鶯	W							1					1	2	
Great Tit	大山雀	R													0	√
Japanese White-eye	暗綠繡眼鳥	R,?W		1			2				2	2	1		8	√
Scaly-breasted Munia	斑文鳥	R										9			9	
Eurasian Tree Sparrow	麻雀	R	2		1	1		2			3	2	5	4	20	
Black-collared Starling	黑領椋鳥	R			1	1			1		1	2		1	7	√
White-shouldered Starling	灰背椋鳥	M,W,Su											1		1	
Common Myna	家八哥	R	1												1	
Crested Myna	八哥	R	1	1		2		3			1		4	1	13	
Common Magpie	喜鵲	R						1							1	
No. of Birds at Each Pond:			**12**	**9**	**8**	**6**	**7**	**15**	**26**	**6**	**32**	**30**	**36**	**21**		
No. of Birds Recorded from Pond Count:			**208**													
No. of Species Recorded from Pond Count:			**31**													
Total No. of Species:			**34**													
Total No. of Species of Conservation Interest:			**1**													

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; Su=summer visitor; M=migrant; Sp=spring; P=present all year; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al* . (2001): The Avifauna of Hong Kong]

Appendix G Bird Species and Abundance Recorded during the Avifauna Monitoring in April 2011

Works Area: TUW
Survey Site: TUW-1
Survey Date: 19 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location							Sub-total	Walk Transect
			TUW-1/P1	TUW-1/P2	TUW-1/P3	TUW-1/P4	TUW-1/P5	TUW-1/P6	TUW-1/P7		
Cattle Egret	牛背鷺	P		1		2		1		4	√
Chinese Pond Heron	池鷺	P				2	1		3	6	
Black Kite	黑鳶(蠅鷹)	W,R								0	√
White-breasted Waterhen	白胸苦惡鳥	R						1	3	4	√
Spotted Dove	珠頸斑鳩	R	3	3	3		1	3	1	14	√
Large Hawk Cuckoo	鷹鵑	Su	1							1	
Common Koel	噪鵑	Su,R				1	1	1		3	√
Greater Coucal	褐翅鴉鵑	R		1				1		2	
Barn Swallow	家燕	SpM,Su	3	5	3	8	2	3	6	30	
Grey Wagtail	灰鶺鴒	W		1						1	
White Wagtail	白鶺鴒	W,R	1		1	2				4	
Olive-backed Pipit	樹鷚	W								0	√
Red-whiskered Bulbul	紅耳鵯	R	6	6	3	8	7	2	3	35	√
Chinese Bulbul	白頭鵯	R	1	1			3		3	8	√
Long-tailed Shrike	棕背伯勞	R		1		1		1		3	
Oriental Magpie Robin	鵲鴝	R	1	4		1	1			7	√
Common Stonechat	黑喉石鴴	W,M				1				1	
Masked Laughingthrush	黑臉噪鶥	R		3			1	1		5	
Yellow-bellied Prinia	黃腹山鷦鶯	R	2	2	3	2	2	5	6	22	√
Plain Prinia	純色山鷦鶯	R			1		1	1		3	
Common Tailorbird	長尾縫葉鶯	R		1						1	√
Dusky Warbler	褐柳鶯	W						1		1	
Japanese White-eye	暗綠繡眼鳥	R,?W	2						1	3	
Scaly-breasted Munia	斑文鳥	R								0	√
Eurasian Tree Sparrow	麻雀	R	10	10	7	3				30	√
Black-collared Starling	黑領椋鳥	R	1	3	1			1		6	
White-shouldered Starling	灰背椋鳥	M, W, Su		1	2			2	4	9	√
Common Myna	家八哥	R				1				1	
Crested Myna	八哥	R			1					1	√
No. of Birds at Each Point:			**31**	**43**	**25**	**32**	**20**	**24**	**30**		
No. of Birds Recorded from Point Count:			**205**								
No. of Species Recorded from Point Count:			**26**								
Total No. of Species:			**29**								
Total No. of Species of Conservation Interest:			**1**								

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; Su=summer visitor; M=migrant; A=autumn; Sp=spring; P=present all year; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al*. (2001): The Avifauna of Hong Kong]

Works Area: TUW and PHV
Survey Site: TUW-2 and PHV-1 (grouped together due to overlapping of survey area)
Survey Date: 19 April 2011

Common Name [1]	Chinese Name	Principal Status [2]	Point Count Location		Sub-total	Walk Transect
			TUW-2 and PHV-1/P1	TUW-2 and PHV-1/P2		
Spotted Dove	珠頸斑鳩	R		1	1	√
Large Hawk Cuckoo	鷹鵑	Su			0	√
Greater Coucal	褐翅鴉鵑	R			0	√
Common Koel	噪鵑	Su, R			0	√
Barn Swallow	家燕	SpM,Su			0	√
Black-winged Cuckoo-shrike	暗灰鵑鵙	AM,W			0	√
Red-whiskered Bulbul	紅耳鵯	R	3	5	8	√
Chinese Bulbul	白頭鵯	R		2	2	
Chestnut Bulbul	栗背短腳鵯	R,W			0	√
Scarlet Minivet	赤紅山椒鳥	R			0	√
Oriental Magpie Robin	鵲鴝	R	1		1	√
Streak-breasted Scimitar Babbler	棕頸鉤嘴鸝	R	1		1	
Rufous-capped Babbler	紅頭穗鸝	R			0	√
Masked Laughingthrush	黑臉噪鸝	R		1	1	
Yellow-bellied Prinia	黃腹山鷦鶯	R			0	√
Common Tailorbird	長尾縫葉鶯	R	1		1	
Great Tit	大山雀	R	1		1	√
Scarlet-backed Flowerpecker	朱背啄花鳥	R			0	√
Fork-tailed Sunbird	叉尾太陽鳥	R	1		1	√
Japanese White-eye	暗綠繡眼鳥	R,?W	1	1	2	√
No. of Birds at Each Point:			**9**	**10**		
No. of Birds Recorded from Point Count:			**19**			
No. of Species Recorded from Point Count:			**10**			
Total No. of Species:			**20**			
Total No. of Species of Conservation Interest:			**1**			

Note:
(1) Species in bold represents Species of Conservation Interest.
(2) R=resident; W=winter visitor; Su=summer visitor; M=migrant; Sp=spring; ?W=the extent of immigration in winter is unclear
[Principal status was assessed with reference to Carey *et al*. (2001): The Avifauna of Hong Kong]

Appendix H

Representative Photographs of the Avifauna Monitoring

Appendix H Representative Photographs taken during the Avifauna Monitoring in April 2011



Plate 1 Intermediate Egret at Point Count Location MPV-1/P10



Plate 2 Osprey along the Walk Transect of MPV-1 Survey Site



Plate 3 Red-throated Pipit at Point Count Location MPV-1/P5

Appendix H Representative Photographs taken during the Avifauna Monitoring in April 2011



Plate 4 Pond Aeration at Point Count Location MPV-1/P2



Plate 5 Drained pond at Point Count Location MPV-1/P2



Plate 6 Wood Sandpiper at Point Count Location TPP-2/P3

Appendix H Representative Photographs taken during the Avifauna Monitoring in April 2011



Plate 7 Site Investigation Works near Point Count Location TUW-1/P4

Appendix I

Certified Arborist Inspection Record

MTR Express Rail Link, Contract 801

Monthly Audit Inspection Record -- April 2011

Audit of tree works, including tree protection, pruning work, transplanting work, maintenance works in the temporary holding nursery, and compensation tree planting

Date	Contract	Activity Description	Purpose
30/04/2011 29/04/2011 05/05/2011	801 – Siu Lang Shui (Nursery) So Kwun Wat Nursery CLP private plot in Tai Po Kau	Inspection of trees to be transplanted within the contract	Regular monthly audit of tree works
04/05/2011	802 - Nam Cheong Property Parcel 40.2, and Sham Mong Rd Footpath, Private Lot NKIL6436	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
04/05/2011	803C Parcels 45.1, 45.3, 45.6, 45.7	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
04/05/2011	805 - Sham Mong Road Parcel 41.4,38.3, Sham Mong Road Footpath (near 38.3), and Footpath of Sham Mong Rd, Parcels 38.6/38.7 (footpath alongside CLP Building) NKIL 6363 (CLP Building)	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
03/05/2011	811A—WKT station North Ngo Cheung Road, Hoi Wang Road, Lin Cheung Road	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
03/05/2011	811B - WKT Approach Tunnels – South Parcel 44.1, Lin Cheung Road, and Jordan Road Footpath & Central Divider	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
30/04/2011	820 - Mei Lai Road to Hoi Ting Road Tunnels Parcel 37.2, 37.3, Kwai Chung Road (Footpath near 37.5) Sham Mong Road & Hing Wah Street West Footpath	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works

	Parcel 39.1, 40.4, Sham Mong Road (Nam Cheong Park) Private Lot STT-KX2382, Private Lot STT-KX2416		
04/05/2011	821—Shek Yam to Mei Lai Road Tunnels Parcel NT-9 (slope) NT-10	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
03/05/2011 (Pat Heung) 05/05/2011 (Kwai Chung, Shek Yam) 29/04/2011	822 - Tse Uk Tsuen to Shek Yam Tunnels Parcels NT-6 (Pat Heung), NT-7, and NT-8, Site Office - San Kwai Street, Kwai Hing, Parcel NT-17 (6.6, 6.9) 822—Siu Lam FW Service Reservoir	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
03/05/2011	823A - Kam Tin Tunnels Parcels NT-5A, NT-5.1A, and NT-5.3A	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
03/05/2011	823B - SSS and ERS Parcels NT-5.1B, NT-5.2, and NT-5.3B	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
05/05/2011	824 Ngau Tam Mei to Tai Kong Po Tunnels NT-3, NT-5.1A, NT-4	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
26/04/2011	825 - Mai Po to Ngau Tam Mei Tunnels Parcels NT-1a (Mai Po), CP-12, and verges of Castle Peak Road - Mai Po	Inspection of retained trees and trees to be transplanted within the contract	Regular monthly audit of tree works
26/04/2011	826 – Mai Po Site Office Parcels NT-1a	Inspection of transplanted trees within the contract	Regular monthly audit of tree works

Signed by:
Matthew PRYOR (RLA, CA)



Appendix J

Landfill Gas Monitoring Record at Rambler Channel Barging Point

Model: GA2000

Manufacturer: Geotechnical Instruments


Serial No: GA08936106

Last Calibration: 01/03/2011

Site Location: Rambler Channel Barging Point, Kwai Yue Lane, Kwai Chung

Date	*Time*	*Performed by*	*Baro Pressure (mb)*	*CH_4 %*	*CO_2 %*	*O_2 %*	*Remarks*
27/04/2011	/	Pak	/	0.0	0.0	19.5	/
29/04/2011	/		/	0.0	0.0	20.6	/

Reviewed / Checked by: Valentino Ho
05-May-2011

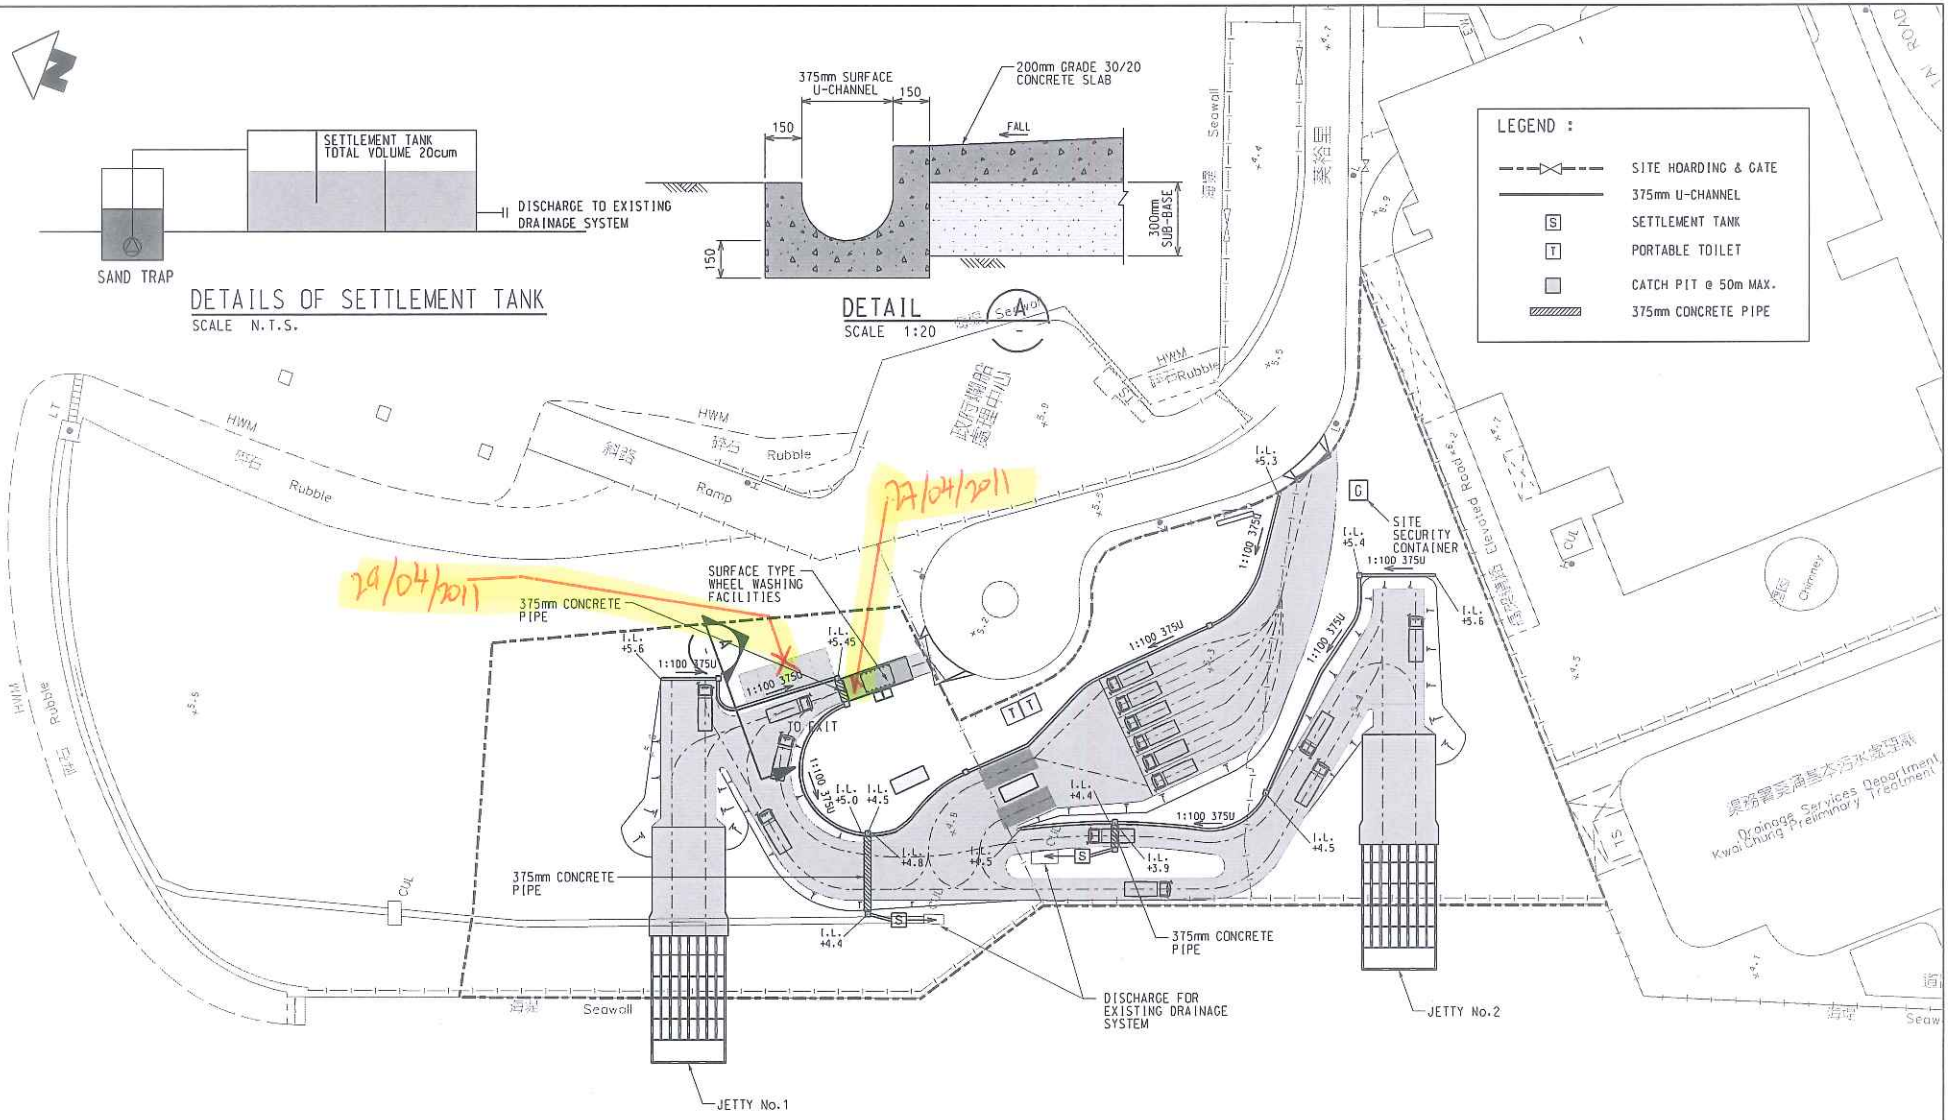

REV	DESCRIPTION	BY	DATE	APPROVED
E	GENERAL REVISION - DARINAGE LAYOUT REVIEWED	CCH	20APR11	PDA
D	U-CHANNEL SIZE REVIEWED	CCH	30MAR11	PDA
C	DRAINAGE DETAILS REVISED	CCH	08MAR11	PDA
B	CATCH PIT ADDED	CCH	16FEB11	PDA
A	FIRST ISSUE FOR SUBMISSION	CCH	30NOV10	PDA

DRAWN	CCH
DESIGNED	ACH
CHECKED	ACH
APPROVED	PDA
DATE	30NOV10

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
©MTR CORPORATION LIMITED 2008 COPYRIGHT ON RESPECT OF THIS DRAWING / DOCUMENT IS OWNED BY THE MTR CORPORATION LIMITED OF HONG KONG. NO REPRODUCTION OF THE DRAWING / DOCUMENT OR ANY PART THEREOF WHETHER MEMO. IS PERMITTED WITHOUT THE PRIOR WRITTEN CONSENT OF THE MTR CORPORATION LIMITED.

MTR

EXPRESS RAIL LINK

ORIGINATOR

MAEDA - CHINA STATE JOINT VENTURE

CADD REF. 823B.C.350.MCJ.T12.021E.dgn

TITLE

CONTRACT 823B
SHEK KONG STABLING SIDINGS AND ERS
RAMBLER CHANNEL BARGING POINT
TEMPORARY DRAINAGE SYSTEM
LAYOUT PLAN

SCALE 1 : 800 (A3)

DRAWING NO. 823B/C/350/MCJ/T12/021

REV. E

MODEL NAME: 25TFALL
FILE NAME: Z:\Dwgs\...\823B\T12_Lamp...\Drainage 1823B.C.350.MCJ.T12.021E.dgn
PRINTED BY: LEUNG CHI
4/29/2011 4:08:58 PM

CERTIFICATION OF CALIBRATION

ISSUED BY: GEOTECH LABORATORY

Date Of Calibration: 1 March, 2011

Certificate Number: GA08936_2/7007

Approved by Signatory

Phil Handy

Laboratory Inspection

GEOTECHNICAL INSTRUMENTS (UK) LTD
Sovereign House, Queensway, Leamington Spa, WarwickShire, CV31 3JR United Kingdom
Tel: +44 (0) 1926 338111 Fax: +44 (0) 1926 338110
E-mail: service@geotech.co.uk Web site: www.geotech.co.uk

Customer: ***Geotechnical Instruments (HK) Ltd***
Unit 9,
9/F Worldwide Industrial Centre
43-47 Shan Mei Street
Fo Tan
Shatin, N. T.,
HONG KONG

Description: Gas Analyser

Model: GA2000
Serial Number: GA08936

Methane (CH4)	
Certified Gas (%)	Instrument Reading (%)
50.01	49.66
15.01	15.10
5.01	5.10

Carbon Dioxide (CO2)	
Certified Gas (%)	Instrument Reading (%)
49.99	50.22
14.97	14.78
5.00	4.86

Oxygen (O2)	
Certified Gas (%)	Instrument Reading (%)
21.00	21.07

Barometer (mb)	
Reference	Reading
1033mb	1033mb

Additional Gas Cells		
Gas	Instrument Reading (ppm)	Certified Gas (ppm)
H^2S	50.6	50.70
CO	516.1	515.0

All concentrations are molar.
CH4, CO2 readings recorded at: 27.6°C
O2 readings recorded at : 17.3°C
Barometric Pressure : 1033mb

Method of Test: The analyser is calibrated in a temperature controlled chamber using reference gases.

End of Certificate
