Drainage Improvement Works Near Four Villages in Yuen Long – Sung Shan New Village, Tai Wo, Lin Fa Tei and Ha Che

Quarterly Environmental Monitoring and Audit (EM&A) Report – November 2024 to January 2025

Wing Tat Civil Engineering Co. Limited

Revision: 2

2025-03-04

aurecon

Bringing ideas to life

MOTT MACDONALD

Drainage Services Department
Project Management Division
42/F Revenue Tower
5 Gloucester Road
Wanchai, Hong Kong

By E-mail

Attn: Mr. Ken Ho

Your Reference

Our Reference
TC/LL/hc/601100222/L070

3/F, Manulife Place,
348 Kwun Tong Road,
Kwun Tong,
Kowloon,
Hong Kong

T +852 2828 5757
F +852 2827 1823
mottmac.com

Contract No. PM 10/2022 -
Independent Environmental Checker for Drainage Improvement Works at Yuen Long – Stage 2

Verification of Quarterly EM&A Report (Nov 2024 to Jan 2025)

11 March 2025

Dear Sir,

We refer to the Quarterly EM&A Report under the captioned Project, which was certified on 4 March 2025 by the Environmental Team Leader appointed under Condition 2.1 of the Environmental Permit No. EP-596/2021 (hereinafter referred to as "EP").

We would like to inform you that we have no adverse comment on the captioned submission. Therefore, we hereby verify the abovementioned submission in accordance with EP Condition 1.9 and Section 12.3 under the Updated EM&A Manual.

Should you have any queries regarding the captioned, please contact our Hin Chan at 2828 5764 or the undersigned at 2828 5751.

Yours faithfully
for MOTT MACDONALD HONG KONG LIMITED



Liz LO
Independent Environmental Checker
T 2828 5751
Liz.lo@mottmac.com

Document control record

Document prepared by:

Aurecon Hong Kong Limited

Unit 1608, 16/F, Tower B, Manulife Financial Centre,
223 – 231 Wai Yip Street, Kwun Tong, Kowloon
Hong Kong S. A. R.

T +852 3664 6888
F +852 3664 6999
E hongkong@aurecongroup.com
W aurecongroup.com

A person using Aurecon documents or data accepts the risk of:

a) Using the documents or data in electronic form without requesting and checking them for accuracy against the original hard copy version.

b) Using the documents or data for any purpose not agreed to in writing by Aurecon.

Document control						aurecon
Report title		Quarterly Environmental Monitoring and Audit (EM&A) Report – November 2024 to January 2025				
Document code		QEM&A-04	**Project number**		P525672	
File path						
Client		Wing Tat Civil Engineering Co. Limited				
Client contact			**Client reference**			
Rev	**Date**	**Revision details/status**	**Author**	**Reviewer**	**Verifier** (if required)	**Approver**
0	2025-02-12	Draft	Jason Man	F. C. Tsang		Kevin Li
1	2025-02-25	Frist Version	Jason Man	F. C. Tsang		Kevin Li
2	2025-03-04	Second Version	Jason Man	F. C. Tsang		Kevin Li
Current revision		**2**				

Approval			
Author signature		Certified by	
Name	Jason Man	Name	F. C. Tsang
Title	Environmental Team Consultant	Title	Environmental Team Leader

Contents

EXECUTIVE SUMMARY ..... **IV**

1 INTRODUCTION **1**

1.1 Project Background 1
1.2 Construction Works Programme 2
1.3 Project Organisation 2
1.4 Construction Works Programme and Construction Works Area 3
1.5 Works undertaken during the Period 3

2 WATER QUALITY **5**

2.1 Monitoring Requirement 5
2.2 Monitoring Location 5
2.3 Monitoring Parameter and Frequency 6
2.4 Action and Limit Level for Water Quality Monitoring 6
2.5 Event and Action Plan 8
2.6 Results and Observations 8
2.7 Quarterly Assessment of Construction Impacts on Suspended Solids at the Project Site 8

3 NOISE **11**

3.1 Monitoring Locations 11
3.2 Noise Monitoring Parameter, Frequency and Duration 11
3.3 Action and Limit Levels 12
3.4 Results and Observations 12

4 ECOLOGY **13**

4.1 Freshwater Crab 13

5 WASTE MANAGEMENT **15**

6 LAND CONTAMINATION **16**

7 LANDSCAPE AND VISUAL **17**

7.1 Audit Requirements 17
7.2 Results and Observations 17

8 CULTURAL HERITAGE **18**

8.1 Archaeology 18
8.2 Built Heritage 19

9 ENVIRONMENTAL SITE INSPECTION AND AUDIT **13**

9.1 Implementation Status of Environmental Mitigation Measures 13

10 SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS **15**

10.1 Summary of Exceedance 15
10.2 Summary of Environmental Non-Compliance 15
10.3 Summary of Environmental Complaint 15
10.4 Summary of Environmental Summon and Successful Prosecution 16

11 CONCLUSIONS AND RECOMMENDATIONS **17**

11.1 Conclusion 17
11.2 Comments/ Recommendations 18

Appendices

APPENDIX 1.1 CONSTRUCTION PROGRAMME

APPENDIX 1.2 PROJECT ORGANIZATION CHART

APPENDIX 2.1 EVENT AND ACTION PLANS FOR WATER QUALITY

APPENDIX 2.2 GRAPHICAL PRESENTATION OF WATER QUALITY MONITORING

APPENDIX 3.1 EVENT AND ACTION PLANS FOR NOISE

APPENDIX 3.2 GRAPHICAL PRESENTATION OF NOISE MONITORING

APPENDIX 5.1 WASTE FLOW TABLE

APPENDIX 10.1 COMPLAINT LOG

Figures

Figure 1.1 General Site Location Plan
Figure 1.2 Location of Work Areas for the Project
Figure 2.1 Impact Water Quality Monitoring Locations
Figure 3.1 Impact Noise Monitoring Locations
Figure 8.1 Area for Archaeological Survey
Figure 8.2 Layout plan showing distance between the works area at Ha Che and the Lan Fong Study Hall

Tables

Table A1 Summary of Exceedance Records of Water Quality Monitoring
Table 1.1 Parties Involved in Project Organisation
Table 2.1 Summary of Impact Water Quality Monitoring Stations
Table 2.2 Parameters measured in the Impact Water Quality Monitoring
Table 2.3 Action and Limit Levels for Water Quality
Table 2.4 Action and Limit Levels of Water Quality
Table 2.5 Summary of Exceedance Records of Water Quality Monitoring
Table 3.1 Noise Monitoring Stations during Construction Phase
Table 3.2 Construction Noise Monitoring Parameter, Frequency and Duration
Table 3.3 Action and Limit Levels for Construction Noise Monitoring
Table 8.1 Mitigation Measures for Impacted Graded Historic Buildings
Table 9.1 Site Observations
Table 10.1 Summary of Exceedance Records of Water Quality Monitoring

Executive Summary

A1. Drainage Services Department (DSD) has appointed Aurecon Hong Kong Limited (Aurecon) to undertake the Environmental Team services for the project and implement the EM&A works.

A2. The construction works commenced on 20 February 2024.

A3. This 4th Quarterly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2022/02 Drainage Improvement Works at Yuen Long – Stage 2 (hereinafter called the "Contract"). The report summaries the findings of the EM&A programme during the reporting period from 1 November 2024 to 31 January 2025.

Key Construction Works in the Reporting Period

A4. A summary of construction activities undertaken during the reporting period is presented below:

Ha Che

- Site Clearance Work
- Breaking Ground
- Temporary Drainage Diversion
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting
- Sheet pilling & Backfilling and Compaction; and
- Removal of Sheet piles, Drain Laying works, Reinstatement

Lin Fa Tei

- Site Clearance Work
- Breaking Ground
- Temporary Drainage Diversion; and
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting; and
- Sheet pilling & Backfilling and Compaction

Sung Shan New Village

- Site Clearance
- Breaking Ground.
- Temporary Drainage Diversion; and
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting; and
- Sheet pilling & Backfilling and Compaction

Tai Wo

- No construction activities (from 1 November to 15 December 2024)
- Site Clearance

Breaches of Environmental Quality Performance Limits (AL levels)

Water Quality

A5. The summary of exceedance records during the reporting period is summarized in **Table A1**.

Table A1 Summary of Exceedance Records of Water Quality Monitoring

Parameter	No. of non-project related exceedances		Total No. of non-project related exceedances	No. of exceedance related to the Project		Total No. of exceedance related to the Project
	AL	LL		AL	LL	
Dissolved Oxygen (DO)	0	0	0	0	0	0
Turbidity	0	0	0	0	0	0
Suspended Solids (SS)	0	0	0	0	0	0

A6. No Action Level or Limit Level exceedance was recorded for water quality monitoring during the reporting period.

Noise

A7. No Action Level or Limit Level exceedance was recorded for construction noise monitoring during the reporting period.

Complaint Log

A8. One environmental complaint regarding air quality and one complaint regarding water quality were received during the reporting period. The relevant investigations are conducting by the related parties. The investigation results will be presented when the investigation has been completed.

Notification of Summons and Successful Prosecutions

A9. No notification of summons or successful prosecutions was received in the reporting period.

Reporting Changes

A10. Construction works at Tai Wo are only allowed during dry season (i.e. October to March) in accordance with Condition 3.2 of EP No. EP-596/2021. Due to no construction activities conducted at Tai Wo from 1 November 2024 to 15 December 2024, no impact noise monitoring, impact water quality monitoring and weekly site inspection at Tai Wo was carried out during the above period. Impact noise monitoring, impact water quality monitoring and weekly site inspection at Tai Wo were resumed starting from 16 December 2024.

1 Introduction

1.1 Project Background

1.1.1 The Drainage Master Plan Studies for the Yuen Long, Kam Tin, Ngau Tam Mei and Tin Shui Wai Drainage Basin (YLDMP) were completed in 1998. The majority of the improvement works in Yuen Long and Kam Tin recommended under the YLDMP Study have been completed. Since completion of the DMP Studies, there have been changes in developments within the areas and new development proposals and town planning studies were commissioned. In addition, some new flooding complaints were received at the upstream areas of the drainage basins, indicating that further improvement to the drainage systems was required.

1.1.2 The Drainage Services Department (DSD) commissioned the "Review of Drainage Master Plans in Yuen Long and North Districts – Feasibility Study" (the Review Study) in 2008 so that the new development scenarios could be incorporated and the effectiveness of the previously recommended works could also be assessed. The Review Study completed in end 2011 identified that some areas in Yuen Long District could not meet the required flood protection level according to the latest land use changes and future developments taking into account various factors, including sedimentation at the downstream main channels, mangrove growth at river estuaries, updated extreme sea level statistics at Tsim Bei Tsui and projected climate change impacts, in the hydraulic analysis. To account for the severity and extent of possible flooding and the works implementation time, the Review Study proposed drainage improvement works in Yuen Long District.

1.1.3 Atkins China Ltd (ACL) was commissioned by the DSD in November 2013 to undertake an Investigation, Design and Construction Consultancy entitled "Agreement No. CE 22/2013 (DS) Drainage Improvement Works in Yuen Long, Stage 1 – Investigation, Design and Construction" (hereinafter called the Assignment). The Project comprises construction of drainage improvement works to four villages (namely Sung Shan New Village, Tai Wo, Lin Fa Tei and Ha Che) including landscaping, waterscaping, utilities diversion, temporary traffic arrangements, re-provisioning / improvements to existing dry weather flow intercepting system and any other works incidental to the completion of the Project.

1.1.4 An Environmental Impact Assessment (EIA) Study Brief (ESB-279/2014) for four villages namely Ha Che, Tai Wo, Lin Fa Tei and Sung Shan New Village which is a designated project was issued by the Environmental Protection Department (EPD) on 14 October 2014.

1.1.5 The EIA Report for Drainage Improvement Works Near Four Villages in Yuen Long – Sung Shan New Village, Tai Wo, Lin Fa Tei and Ha Che (referred to as "the Project") (Register No. AEIAR-229/2021) was approved on 3 June 2021 and the Environmental Permit (EP) EP-596/2021, covering the Upgrading, Construction and Deepening of the Project was granted on 28 September 2021.

1.1.6 Aurecon Hong Kong Limited (Aurecon) is commissioned by the Wing Tat Civil Engineering Co. Limited to undertake the Environmental Team (ET) services and carry out the Environmental Monitoring and Audit (EM&A) for Drainage Improvement Works Near Four Villages in Yuen Long - Sung Shan New Village, Tai Wo, Lin Fa Tei and Ha Che (Register No. EP-596/2021).

1.1.7 This is the 4th Quarterly EM&A Report summarizing the key findings of the construction phase EM&A programme from 1 November 2024 to 31 January 2025 (the reporting period) and is submitted to fulfil the requirements in Section 12.3 of the approved Updated EM&A Manual of the Project.

1.2 Construction Works Programme

1.2.1 The construction programme and the location plan of the Project are shown in **Appendix 1.1** and **Figure 1.1** respectively. The locations of the proposed drainage improvement work at the four villages are presented in **Figures 1.2a** to **Figures 1.2d**.

1.3 Project Organisation

1.3.1 Involvement of relevant parties in a collaborative and interactive manner is essential for the implementation of the recommended EM&A programme. The following sections outline the primary responsibilities and duties of the key EM&A programme participants. The lines of communication with respect to EM&A works are shown in **Diagram 1.1**.

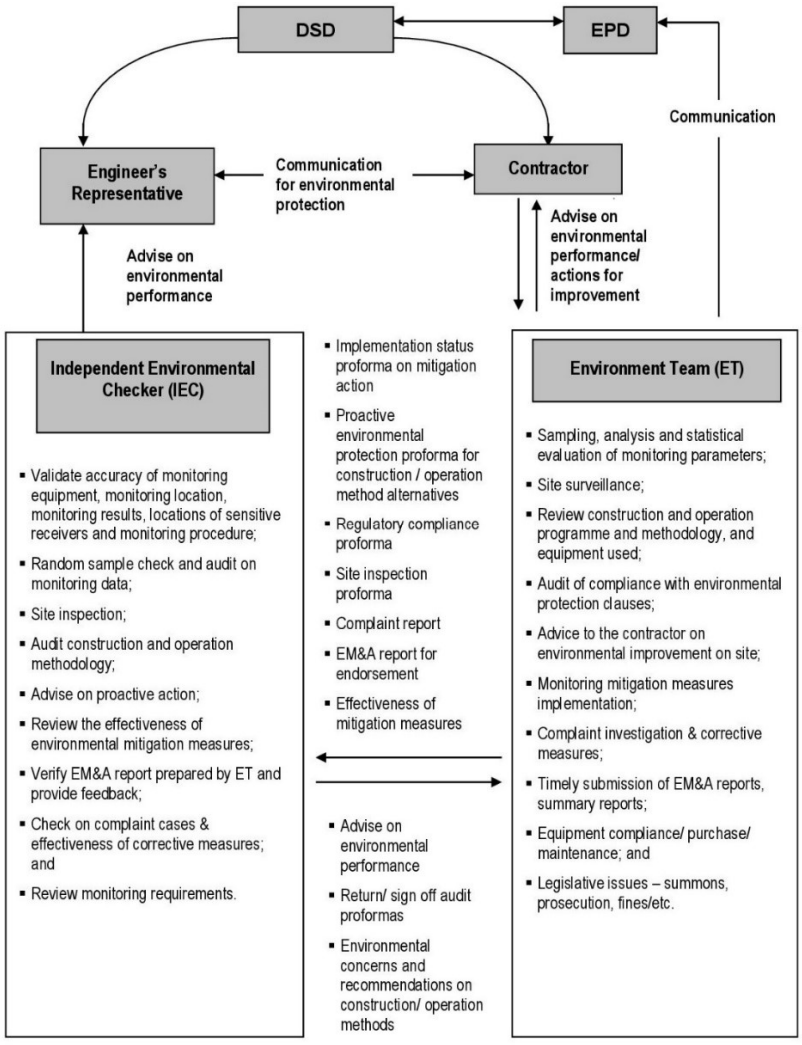


Diagram 1.1 Organisation Chart

1.3.2 Parties with different levels of involvement in the Project organisation are summarized in **Table 1.1**.

Table 1.1 Parties Involved in Project Organisation

Parties	Organization / Company
Project Proponent	Drainage Services Department
Supervisor / Engineer's Representative (ER)	Atkins China Ltd
Contractor	Wing Tat Civil Engineering Co. Limited
Environmental Team (ET)	Aurecon Hong Kong Limited
Independent Environmental Checker (IEC)	Mott MacDonald Hong Kong Limited

1.3.3 The key personnel contact names and numbers are summarized in **Appendix 1.2**.

1.4 Construction Works Programme and Construction Works Area

1.4.1 The construction works commenced on 20 February 2024. The construction works programme and the construction works area of the Project are shown in **Appendix 1.1** and **Figure 1.1** respectively.

1.5 Works undertaken during the Period

1.5.1 The main construction works carried out in the reporting period were as below.

Ha Che

- Site Clearance Work
- Breaking Ground
- Temporary Drainage Diversion
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting
- Sheet pilling & Backfilling and Compaction; and
- Removal of Sheet piles, Drain Laying works, Reinstatement

Lin Fa Tei

- Site Clearance Work
- Breaking Ground
- Temporary Drainage Diversion; and
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting; and
- Sheet pilling & Backfilling and Compaction

Sung Shan New Village

- Site Clearance
- Breaking Ground.
- Temporary Drainage Diversion; and
- Excavation and Lateral Support, Relocate/ Divert Utilities, Rebar Fixing, Formwork Erection and Cast-in, Concreting; and
- Sheet pilling & Backfilling and Compaction

Tai Wo

- No construction activities (from 1 November to 15 December 2024)
- Site Clearance

1.5.2 The environmental mitigation measures corresponding to the main construction works implemented in the reporting period can be referred to **Appendix 1.3**.

2 Water Quality

2.1 Monitoring Requirement

2.1.1 In accordance with the approved Updated EM&A Manual, impact water quality monitoring should be carried out three days per week at all designated monitoring stations during the construction period. The interval between two sets of monitoring should not be less than 36 hours.

2.1.2 Replicate in-situ measurements of dissolved oxygen (DO), temperature, pH, turbidity, salinity, water depth and suspended solids (SS) for each independent sampling event shall be collected to ensure a robust statistically interpretable database.

2.2 Monitoring Location

2.2.1 Impact water quality monitoring was conducted at 8 monitoring stations (except Station C4 & C5) from 1 November to 15 December 2024 and conducted at 10 monitoring stations from 16 December 2024 to 31 January 2025 which is summarized in **Table 2.1**. The location of water quality monitoring stations is shown in **Figure 2.1a** to **Figure 2.1d**.

Table 2.1 Summary of Impact Water Quality Monitoring Stations

Stream	Monitoring ID	Coordinates (HK Grid)		Remarks
		Easting	Northing	
SSNV	C1A (1)	821702	831945	Alternative Impact Monitoring Point
	C2	822459	831470	Control Monitoring Point
	C3A (2)	822413	831284	Alternative Control Monitoring Point
TW	C4 (4)	825497	830664	Control Monitoring Point
	C5 (4)	825486	830716	Impact Monitoring Point
LFT	C6	827232	831713	Control Monitoring Point
	C7A (3)	826865	832115	Alternative Control Monitoring Point
	C8	826513	832075	Impact Monitoring Point
HC	C9	828304	835029	Control Monitoring Point
	C10	827919	834271	Impact Monitoring Point

Notes:

(1) At Station C1, access to safe sampling of water is not feasible due to steep banks on both sides of the stream channel. An alternative monitoring location is proposed at Station C1A, which is about 250 m along the same stream channel downstream of Station C1 and is accessible for safe water sampling.

(2) During the first day of baseline monitoring at Station C3, shallow water was observed, and the ET could not sample enough water for monitoring. As agreed by the ER, the Contractor, and the IEC, a new sampling location, Station C3A, was identified at about 130 m upstream and was accessible for water sampling.

(3) For Station C7, the location is not close to the nearest, revised works boundary (about 200 m away). An alternative monitoring location is proposed at Station C7A, which is about 23 m upstream of the nearest, revised works boundary.

(4) Construction works at Tai Wo are only allowed during dry season (i.e. October to March) in accordance with Condition 3.2 of EP No. EP-596/2021. Due to no construction activities conducted at Tai Wo from 1 November 2024 to 15 December 2024, no impact water quality monitoring at Tai

Wo was carried out during the above period. Impact water quality monitoring at Tai Wo were resumed starting from 16 December 2024.

2.3 Monitoring Parameter and Frequency

2.3.1 The monitoring parameters, frequency and duration of impact water quality monitoring are listed in **Table 2.2**.

Table 2.2 Parameters measured in the Impact Water Quality Monitoring

Parameter	Frequency	Duration	Stream	Monitoring ID
Dissolved oxygen (DO), temperature, turbidity, salinity, pH, stream water depth and suspended solids (SS)	Before 2 Dec 2024: 3 days in a week; After 1 Dec 2024: 1 day in a week (1)	Throughout the construction phase	SSNV	C1A
				C2
				C3A
			LFT	C6
				C7A
				C8
			HC	C9
				C10
	3 days in a week		TW	C4
				C5

Notes:
(1) Impact monitoring shall be carried out 3 days per week during the construction process. The monitoring frequency can be reduced to once per week, with sampling/ measurement at the designated monitoring locations when no exceedances were recorded during the past three-month period in accordance with Section 2.7, Appendix 4 of the Updated EM&A Manual. The change of the monitoring frequency at SSNV, LFT and HC was approved by EPD on 25 November 2024. Hence, the monitoring frequency at SSNV, LFT and HC was changed to 1 day in a week starting from 2 December 2024.

2.3.2 Monitoring location and position, time, sampling depth, weather conditions and any special phenomena or work underway nearby are recorded during the impact monitoring.

2.4 Action and Limit Level for Water Quality Monitoring

2.4.1 The criteria of action and limit levels for water quality monitoring are defined in **Table 2.3**.

Table 2.3 Action and Limit Levels for Water Quality

Parameters	Action Level	Limit Level
DO in mg/L	< 5%-ile of baseline data	< 4 mg/L or < 1%-ile of baseline data
SS in mg/L	> 95%-ile of baseline data or >120% of upstream control station of the same day, whichever is higher	> 99%-ile of baseline data or 130% of upstream control station of the same day, whichever is higher
Turbidity in NTU	> 95%-ile of baseline data or >120% of upstream control station of the same day, whichever is higher	> 99%-ile of baseline data or > 130% of upstream control station of the same day, whichever is higher

Notes:
(1) For DO, non-compliance of the water quality limit occurs when monitoring result is lower than the limit.
(2) For SS and turbidity, non-compliance of the water quality limit occurs when monitoring result is higher than the limit.
(3) All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered necessary.

2.4.2 Based on the criteria listed in **Table 2.3**, the action and limit levels for water quality are determined in **Table 2.4**.

Table 2.4 Action and Limit Levels of Water Quality

Stream	Monitoring ID	Parameters	Action	Limit
SSNV	C1A	DO in mg/L	<6.72	<4 (1)
		SS in mg/L	>7.3 or >120% of upstream control station of the same day, whichever is higher	>8.5 or > 130% of upstream control station of the same day, whichever is higher
		Turbidity in NTU	>10.37 or >120% of upstream control station of the same day, whichever is higher	>10.81 or > 130% of upstream control station of the same day, whichever is higher
TW	C5	DO in mg/L	<8.36	<4 (2)
		SS in mg/L	>9.9 or > 120% of upstream control station of the same day, whichever is higher	>10.0 or > 130% of upstream control station of the same day, whichever is higher
		Turbidity in NTU	>13.64 or > 120% of upstream control station of the same day, whichever is higher	>13.87 or > 130% of upstream control station of the same day, whichever is higher
LFT	C8	DO in mg/L	<5.38	<4 (3)
		SS in mg/L	>6.3 or > 120% of upstream control station of the same day, whichever is higher	>7.0 or > 130% of upstream control station of the same day, whichever is higher
		Turbidity in NTU	>12.46 or > 120% of upstream control station of the same day, whichever is higher	>12.94 or > 130% of upstream control station of the same day, whichever is higher
HC	C10	DO in mg/L	<2.55	<2.43 (4)
		SS in mg/L	>8.7 or > 120% of upstream control station of the same day, whichever is higher	>8.8 or > 130% of upstream control station of the same day, whichever is higher
		Turbidity in NTU	>20.06 or > 120% of upstream control station of the same day, whichever is higher	>21.07 or > 130% of upstream control station of the same day, whichever is higher

Notes:

(1) The 1%-ile of baseline DO data at C1A is 6.61 mg/L, which is higher than 4 mg/L. Thus, DO concentration of 4 mg/L, which is in line with the Water Quality Objectives, is adopted as the limit level.

(2) The 1%-ile of baseline DO data at C5 is 8.09 mg/L, which is higher than 4 mg/L. Thus, DO concentration of 4 mg/L, which is in line with the Water Quality Objectives, is adopted as the limit level.

(3) The 1%-ile of baseline DO data at C8 is 5.36 mg/L, which is higher than 4 mg/L. Thus, DO concentration of 4 mg/L, which is in line with the Water Quality Objectives, is adopted as the limit level.

(4) The 1%-ile of baseline DO data at C10 is 2.43 mg/L, which is lower than 4 mg/L. Taking account of the baseline water quality condition and to minimise any false alarm of water quality deterioration during construction phase, DO concentration of 2.43 mg/L is adopted as the limit level.

2.5 Event and Action Plan

2.5.1 Should any non-compliance of the criteria occur, action in accordance with the Event and Action Plan in **Appendix 2.1** shall be followed. Investigation of the exceedances of environmental quality performance limits should be conducted, and the ET will immediately notify the IEC and EPD, as appropriate. The notification should be followed up with advice to the IEC and EPD on the results of the investigation, proposed actions and success of the action taken, with any necessary follow-up proposals.

2.6 Results and Observations

2.6.1 The detailed monitoring results during the reporting period are reported in the monthly EM&A Reports. The graphical presentation of water quality monitoring at the monitoring stations are shown in **Appendix 2.2**.

2.6.2 No Action or Limit Level exceedances was recorded during the reporting period.

2.6.3 The summary of exceedance records of water quality monitoring during the reporting period is summarized in **Table 2.5**.

Table 2.5 Summary of Exceedance Records of Water Quality Monitoring

Parameter	No. of non-project related exceedances		Total No. of non-project related exceedances	No. of exceedance related to the Project		Total No. of exceedance related to the Project
	AL	LL		AL	LL	
Dissolved Oxygen	0	0	0	0	0	0
Turbidity	0	0	0	0	0	0
Suspended Solids	0	0	0	0	0	0

2.7 Quarterly Assessment of Construction Impacts on Suspended Solids at the Project Site

2.7.1 The comparison of the difference between the quarterly mean and 1.3 times of the ambient mean is presented in **Table 2.6**.

Table 2.6 Comparison of the difference between the quarterly mean and 1.3 times of the ambient mean

Parameter	Monitoring Location	Quarterly Mean of SS (mg/L)	Baseline Level of SS (mg/L)	1.3 Times of Ambient Mean (mg/L) (1)	Quarterly Mean of SS > 1.3 Times of Ambient Mean (Y/N)	Request of Further Mitigation Measures (Y/N)
Suspended Solids	C1A	3.5	4.8	6.2	N	N
	C2 (Control Point)	5.7	3.2	4.2	Y	N/A
	C3A (Control Point)	4.9	2.2	2.9	Y	N/A
	C4 (Control Point)	10.4	10.7	13.9	N	N/A
	C5	7.0	5.2	6.8	Y	Y
	C6 (Control Point)	17.2	3.7	4.8	Y	N/A
	C7A (Control Point)	13.9	6.7	8.7	Y	N/A
	C8	4.1	4.0	5.2	N	N
	C9 (Control Point)	4.8	5.9	7.7	N	N/A
	C10	3.2	8.5	11.1	N	N

Notes:
(1) 1.3 times of the ambient mean equal to be defined as 30% increase of the baseline data.

Sung Shan New Village (Monitoring Locations C1A, C2 & C3A)

2.7.2 The quarterly mean of SS at Monitoring Location C1A (Impact Point) (3.5 mg/L) is lower than the 1.3 times of the ambient mean (6.2 mg/L). Hence, no further mitigation measures for control of water quality impact are required at Sung Shan New Village.

Tai Wo (Monitoring Locations C4 & C5)

2.7.3 The quarterly mean of SS at Monitoring Location C5 (Impact Point) (7.0 mg/L) is higher than 1.3 times of the ambient mean (6.8 mg/L). Although there is no Action Level and Limit Level exceedance during the reporting period, the proposed mitigation measures for control of water quality impact at Tai Wo were properly implemented during the reporting period. These include the silt removal facilities with the discharge license under WPCO provided at Tai Wo to remove silt particles from runoff to meet the requirements of the TM standards under WPCO. The silt removal facilities were maintained and cleaned regularly to ensure the proper function. Deposited silt and grit were removed regularly and disposed of by spreading evenly over stable, vegetated areas. Earthwork surfaces were well compacted and the subsequent permanent work or surface protection was carried out immediately after the final surfaces were formed. The exposed slope surfaces and open stockpiles of construction materials on site were covered by tarpaulin to prevent the washing away of construction materials, soil, silt or debris into any drainage system. Based on above observation during the observation of the weekly site inspections, the proposed mitigation measures for control of water quality impact at Tai Wo were considered effective and efficient in pollution control during the reporting period. The contractor has been reminded that the mitigation measures for control of water quality impact at Tai Wo should continue to be maintained in good effectiveness. The detailed recommended mitigation measures are presented in **Appendix 1.3**.

Lin Fa Tei (Monitoring Locations C6, C7A & C8)

2.7.4 The quarterly mean of SS at Monitoring Location C8 (Impact Point) (4.1 mg/L) is lower than the 1.3 times of the ambient mean (5.2 mg/L). Hence, no further mitigation measures for control of water quality impact are required at Lin Fa Tei.

Ha Che (Monitoring Locations C9 & C10)

2.7.5 The quarterly mean of SS at Monitoring Location C10 (Impact Point) (3.2 mg/L) is lower than the 1.3 times of the ambient mean (11.1 mg/L). Hence, no further mitigation measures for control of water quality impact are required at Ha Che.

3 Noise

3.1 Monitoring Locations

3.1.1 The monitoring locations for construction noise monitoring are listed in **Table 3.1** and shown in **Figure 3.1a** to **Figure 3.1d**.

Table 3.1 Noise Monitoring Stations during Construction Phase

ID No. (1)	Location	Nature of Uses	Type of Measurement
SSNV_M2	Village house next to a nullah in Tong Tai Po Tsuen (near DD118 1720 S.A)	Residential	Façade
SSNV_M3	Village house near a soybean sauce factory in Sung Shan New Village (near DD118 1712)	Residential	Façade
SSNV_M6	#43, Sung Shan New Village	Residential	Free-field
TW_M2 (4)	#200, Cheung Po	Residential	Free-field
TW_M3 (4)	Kai Yip Garden, #3H, Tai Wo	Residential	Free-field
LFT_M1	#2G, Lin Fa Tei	Residential	Façade
LFT_M3A (2)	Near #125B, Lin Fa Tei	Residential	Free-field
LFT_M5	#156B, Lin Fa Tei	Residential	Façade
LFT_M6 (3)	Village house near the nullah (DD112 699 S.E)	Residential	Façade
LFT_M11 (2)	#210, Ngau Keng Tsuen	Residential	Façade
HC_M3A (2)	Next to DD111 326 S.B RP near Fan Kam Road	-	Free-field
HC_M4	#1C, Chuk Hang	Residential	Façade
HC_M6	The Arbutus House 12, #52, Shui Kan Shek	Residential	Façade

Notes:

(1) SSNV – Sung Shan New Village; TW – Tai Wo; LFT – Lin Fa Tei; HC – Ha Che.

(2) LFT_M3A, LFT_M11, HC_M3A and are alternative noise monitoring stations proposed to replace LFT_M3, LFT_M13 and HC_M3, respectively.

(3) Due to the objection from property management office for providing access to designated monitoring location, the noise monitoring at LFT_M7 have been suspended since 27 March 2024. An alternative monitoring location LFT_M6 was proposed to replace LFT_M7 and agreed with the ER and the IEC.

(4) Construction works at Tai Wo are only allowed during dry season (i.e. October to March) in accordance with Condition 3.2 of EP No. EP-596/2021. Due to no construction activities conducted at Tai Wo from 1 November 2024 to 15 December 2024, no impact noise monitoring at Tai Wo was carried out during the above period. Impact noise monitoring at Tai Wo was resumed starting from 16 December 2024.

3.2 Noise Monitoring Parameter, Frequency and Duration

3.2.1 Construction noise level was measured by the ET and measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30mins)}$ used as the monitoring parameter for the construction noise monitoring. The monitoring should be conducted during the construction phase between 0700 and 1900 on normal weekdays at the designated monitoring locations.

3.2.2 As supplementary information for data auditing, statistical results such as L10 and L90 were also obtained for reference.

3.2.3 **Table 3.2** summarizes the monitoring parameters, duration, and frequency of construction noise monitoring.

Table 3.2 Construction Noise Monitoring Parameter, Frequency and Duration

Monitoring Station	Parameter	Frequency and Duration
SSNV_M2, SSNV_M3, SSNV_M6, HC_M3A, HC_M4, HC_M6, TW_M2, TW_M3, LFT_M1, LFT_M3A, LFT_M5, LFT_M6 and LFT_M11	$L_{eq(30mins)}$ (as a logarithmic average of 6 consecutive $L_{eq(5mins)}$)	Once every week throughout the construction phase between 0700 and 1900 on normal weekdays

3.3 Action and Limit Levels

3.3.1 The Action and Limit levels were established in accordance with the approved Updated EM&A Manual. **Table 3.3** presents the Action and Limit Levels for construction noise. Should non-compliance of the criteria occur, action in accordance with the Event and Action Plan presented in **Appendix 3.1** shall be carried out.

Table 3.3 Action and Limit Levels for Construction Noise Monitoring

Time Period	Action	Limit Level
07:00 – 19:00 on normal weekdays	When one or more documented complaints are received	75 dB(A)(1)
07:00 – 23:00 on holidays; and 19:00 – 23:00 on all other days		45 dB(A)(2)
23:00 – 07:00 of the next day		30 dB(A)(2)

Notes:
(1) Between 07:00 and 19:00, construction noise limit for school during normal term time is 70 dB(A) and 65 dB(A) during examination period.
(2) The ASR of identified noise sensitive receivers is “A”, which is a rural area that is not affected by the in Influencing Factors (Ifs). The limit levels are stipulated in the Technical Memorandum on Noise from Construction Work in Designated Areas.

3.4 Results and Observations

3.4.1 The detailed monitoring results during the reporting period are reported in the monthly EM&A Reports. The graphical presentation of noise monitoring at the monitoring stations are shown in **Appendix 3.2**.

3.4.2 No Action or Limit levels exceedance was recorded in the reporting period.

4 Ecology

4.1 Freshwater Crab

4.1.1 With reference to the approved EIA Report (Register No.: AEIAR-229/2021), two freshwater crab species of conservation importance were recorded within the work sites during the ecological baseline survey. *Somanniathelphusa zanklon* was recorded at Lin Fa Tei and Ha Che, while *Cryptopotamon anacoluthon* was recorded in the upstream area at Ha Che. Both species are endemic to Hong Kong and considered to be "Endangered" and "Vulnerable" by the IUCN respectively (IUCN 2023). The construction activities of the project will disturb their natural habitats and potentially causing a direct loss of these two species due to their limited mobility.

Post-translocation Monitoring

4.1.2 According to Section 5.2.5 of the approved Updated EM&A Manual for the Project, monthly post-translocation monitoring shall be conducted for at least 12 months after pre-construction surveys to monitor their establishment.

4.1.3 During the monitoring, active visual search by hand netting and kick sampling for aquatic fauna species would be performed at the respective receptor sites. Potential micro-habitats and hiding spaces that is favoured by the crabs such as rocks, organic debris, leaf litter, and riparian vegetation etc., will also be overturned or raked.

4.1.4 Upon discovery of any marked individuals from the pre-construction survey, date and time of capture, size and health condition of the individual will also be recorded once again.

4.1.5 The practice of mark and recapture of the translocated population of *S. zanklon* and *C. anacoluthon* at the receptor site can then be used to estimate population size, as well as inform the health and survival status of the translocated population.

4.1.6 Post-translocation Monitoring was carried out in the reporting period. The monitoring results are reported in the monthly EM&A Reports prepared for this Contract.

4.1.7 None of the translocated individuals from the pre-construction survey was found in the upper and lower receptor sites of Ha Che or the receptor site of Lin Fa Tei during the reporting period.

4.1.8 However, 2 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper and Ha Che Lower receptor sites in November 2024. These individuals, however, were not the translocated individual as their details (i.e., carapace, sex and species) did not match with any of the translocated individuals in the record.

4.1.9 In addition, 3 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper and Ha Che Lower receptor sites in December 2024. These individuals, however, were not the translocated individual as their details (i.e., carapace, sex and species) did not match with any of the translocated individuals in the record.

4.1.10 Moreover, 2 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper receptor sites in January 2025. These individuals, however, were not the translocated individual as their details (i.e., carapace, sex and species) did not match with any of the translocated individuals in the record.

5 Waste Management

5.1.1 Waste generated from the Project include inert construction and demolition (C&D) materials and non-inert C&D wastes in the reporting period. The amount of waste generated by the construction works of the Project during the reporting period are shown in **Appendix 5.1**.

5.1.2 Sorting of construction and demolition (C&D) materials was carried out on site. Sufficient numbers of receptacles were provided for general refuse collection and sorting. Excavated inert C&D materials were reused to minimize the disposal of C&D waste to public fill.

5.1.3 The Contractor is advised to minimize the wastes generated through recycling or reusing. All applicable mitigation measures stipulated in the approved Updated EM&A Manual and waste management plans will be fully implemented.

6 Land Contamination

6.1.1 With reference to results of land contamination assessment included in the approved EIA Report (Register No.: AEIAR-229/2021), all identified sites with potential contamination are located outside the work area of the Project and no potential contamination arising from the proposed drainage improvement works is anticipated. Therefore, no land contamination issue is anticipated for this Project.

6.1.2 Mitigation measures listed in **Appendix 1.3** should be adopted if any suspended contamination encountered during construction.

6.1.3 No suspected on-site contamination was observed or reported by the Contractor in the reporting period.

7 Landscape and Visual

7.1 Audit Requirements

7.1.1 According to the approved Updated EM&A Manual, site audits should be undertaken every week during the construction phase to check that the proposed landscape and visual mitigation measures are properly implemented and maintained as per their intended objectives. Mitigation measures recommended in the EIA Report as the audit requirements including, preservation of existing vegetation, transplanting of affected trees, compensatory tree planting, control of night-time lighting glare, erection of decorative screen hoarding and management of construction activities and facilities are summarized in **Appendix 1.3**.

7.2 Results and Observations

7.2.1 To monitor and audit the implementation of landscape and visual mitigation measures, 13 weekly landscape and visual site audits were carried out in the reporting period. No deficiency in the mitigation measures on landscape and visual was observed during the reporting period.

8 Cultural Heritage

8.1 Archaeology

8.1.1 According to the assessment included in the approved EIA report (Register No.: AEIAR-229/2021) the proposed drainage works in the Lin Fa Tei area are located immediately adjacent to existing river course on mainly Pleistocene terraced alluvium and the western end of the alignment on Holocene alluvium between Lin Fa Tei Site of Archaeological Interest (SAI) and Shui Lau Tin SAI. The proposed works are partially located within Lin Fa Tei SAI. Previous investigations within SAI have shown both in situ and secondary deposit and with potential for wooden features near the stream bed. As per the recommendation from EIA report, Archaeological Survey shall be conducted prior to the construction works, the concerned area is marked in **Figure 8.1**.

8.1.2 A qualified archaeologist shall be engaged and apply for a licence under the Antiquities and Monuments Ordinance (Cap. 53) to conduct the Archaeological Survey prior to the construction phase. The scope and methodology of the Archaeological Survey shall be agreed with Antiquities and Monuments Office (AMO) prior to implementation. Tentatively and subject to agreement with AMO, a fieldscan, where possible, twenty auger tests and four 5 by 1m narrow trenches are proposed to further assess the archaeological potential of the area. If significant remains are uncovered, AMO should be notified and potential need for mitigation and/ or an appropriate way forward should be agreed by AMO and relevant parties.

8.1.3 For remaining drainage work areas (outside the area identified for Archaeological Survey) deemed to have limited (near Kam Sheung Road) to minimal (remainder of Works Areas) archaeological potential, AMO shall be informed immediately if antiquities or supposed antiquities are discovered during construction works for the proposed drainage improvement works for ascertaining required remedial works.

8.1.4 The licence application for archaeological survey works at Lin Fa Tei, Yuen Long was approved by the AMO on 28 June 2024. The Archaeological Survey at Lin Fa Tei was carried out from 16 to 28 October 2024. During this period, the qualified Archaeologist has excavated five test trenches (5m x 1.2m each in size) coded TT1 to TT5 respectively and executed 20 auger tests coded AH1 to AH20 respectively.

8.1.5 Generally, the fill deposit at the top of the excavated area is modern and formed in recent years; the sludge deposits underneath contain no archaeological remains whatsoever.

8.1.6 Therefore, it can be concluded that there is no archaeological potential in the Licence Area, and the construction works of the Project will not cause any adverse impact to archaeological heritage in this part of the Lin Fa Tei Site of Archaeological Interest. The completion brief of archaeological survey was submitted to AMO for review on 30 October 2024. No comment was received from the AMO up to the end of the reporting period.

8.2 Built Heritage

8.2.1 According to the approved Updated EM&A manual, mitigation measures that should be implemented during the construction phase for graded historic buildings are presented in **Table 8.1**.

8.2.2 Condition surveys were carried out by qualified structural engineer for Lee Tat Bridge, Lan Fong Study Hall and St John's Chapel prior to construction works. The Pre-construction Condition Survey Report were submitted to the EPD on 22 December 2023 under Condition 2.10 of the EP.

8.2.3 Due to the distance between the works area at Ha Che and the Lan Fong Study Hall exceeded 30m radial distance during the reporting period, no vibration monitoring was undertaken. Settlement and tilting monitoring at Lan Fong Study Hall at Ha Che has been carried out during the reporting period (excluded public holiday). The distance between the north works area at Ha Che and the Lan Fong Study Hall is around 395.34m. While the distance between the south works area at Ha Che and the Lan Fong Study Hall is around 63.76m. The layout plan showing distance between the works area at Ha Che and the Lan Fong Study Hall is presented in **Figure 8.2**. No exceedance for relevant monitoring was recorded during the reporting period. No monitoring was carried out at St. John's Chapel near Tai Wo as no construction works were carried out at this district since April 2024. No monitoring has been carried out at Lee Tat Bridge at Lin Fa Tei as the works areas are more than 500 m away. Monitoring data is submitted to the AMO on quarterly basis.

Table 8.1 Mitigation Measures for Impacted Graded Historic Buildings

Graded Historic Buildings	Mitigation Measures
Lee Tat Bridge, Shui Tsan Tin (Grade 3)	▪ A condition survey should be carried out in advance of works and after completion of works by qualified building surveyor or structural engineer. The Condition Survey Report should contain descriptions of the structure, identification of fragile elements, an appraisal of the condition and working methods for any proposed monitoring and precautionary measures that are or were recommended with aid of photo records. The condition survey report must be submitted to the AMO for comment before construction activities commence and after the works have been completed. The contractor should implement the approved monitoring and precautionary measures. ▪ Vibration, settlement and tilting monitoring should be undertaken during the construction works to ensure that safe levels of vibration are not exceeded. An Alert, Alarm and Action (AAA) vibration limit set at 5 / 6 / 7.5 mm/s for Grade 3 historic buildings, settlement limit set at 6/ 8/ 10mm, and tilting limit set at 1/2000; 1/1500; 1/1000 should be adopted. Monitoring proposal, including checkpoint locations, installation details, response actions for each of the AAA levels and frequency of monitoring should be submitted for AMO's consideration. Installation of monitoring checkpoints shall be carried out in great care and adequate protection shall be provided so as to avoid unnecessary disturbance/ damage to the historic fabrics. Photo records of monitoring checkpoints shall be submitted upon installation for AMO's records. Monitoring records should be submitted to AMO on regular basis and alert AMO should the monitoring reach AAA levels.
Lan Fong Study Hall, Chuk Hang (Grade 3)	
St John’s Chapel, Cheung Po (Grade 2)	

9 Environmental Site Inspection and Audit

9.1 Implementation Status of Environmental Mitigation Measures

9.1.1 Site audits were carried out by ET on weekly basis at least once per week to monitor the implementation of proper environmental management practices and mitigation measures in the Project site.

9.1.2 Total 13 site inspections were carried out during the reporting period. No outstanding issues were reported during the reporting period. Details of observations recorded during the site inspections are presented in **Table 9.1**.

Table 9.1 Site Observations

Date	Environmental Observations	Follow-up Status
6 Nov 2024	Observation(s) and Recommendation(s) Nil	 Nil
13 Nov 2024	Observation(s) and Recommendation(s) Lin Fa Tei: 1. Geotextiles should be maintained in good condition and place to the right position. 2. Wastewater should be direct to the wet sep ad the wet sep should be moved to the front to discharge.	 Lin Fa Tei: 1. Geotextiles was maintained in good condition and placed in the right position. 2. Wastewater was directed to the Wet Sep for treatment and was discharged downstream of our work area.
20 Nov 2024	Observation(s) and Recommendation(s) Nil	 Nil
27 Nov 2024	Observation(s) and Recommendation(s) Nil	 Nil
4 Dec 2024	Observation(s) and Recommendation(s) 1. Nil	 1. Nil
11 Dec 2024	Observation(s) and Recommendation(s) Ha Che: 1. The contractor was reminded to display the environmental permit at an appropriate location (e.g. site entrance) instead of the area within the site.	 Ha Che: 1. The environmental permit was displayed at an appropriate location by the contractor.
19 Dec 2024	Observation(s) and Recommendation(s) Nil	 Nil
27 Dec 2024	Observation(s) and Recommendation(s) Nil	 Nil
31 Dec 2024	Observation(s) and Recommendation(s) Ha Che: 1. The decolorized NRMM label should be replaced with a proper label. (BH16)	 Ha Che: 1. The proper NRMM label was attached by the contractor. (BH16)

Date	Environmental Observations	Follow-up Status
8 Jan 2025	Observation(s) and Recommendation(s) Sung Shan New Village: 1. The Contractor was reminded to direct the effluent to sedimentation tank for treatment before discharge.	Sung Shan New Village: 1. The effluent was direct to sedimentation tank for treatment before discharge.
15 Jan 2025	Observation(s) and Recommendation(s) Nil	Nil
22 Jan 2025	Observation(s) and Recommendation(s) Nil	Nil
28 Jan 2025	Observation(s) and Recommendation(s) Nil	Nil

9.1.3 According to the EIA Study Report, Environmental Permit, contract documents and approved Updated EM&A Manual, the mitigation measures detailed in the documents should be implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix 1.3**.

10 Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions

10.1 Summary of Exceedance

Water Quality Monitoring

10.1.1 The summary of exceedance records of water quality monitoring during the reporting period is summarized in **Table 10.1**.

Table 10.1 Summary of Exceedance Records of Water Quality Monitoring

Parameter	No. of non-project related exceedances		Total No. of non-project related exceedances	No. of exceedance related to the Project		Total No. of exceedance related to the Project
	AL	LL		AL	LL	
Dissolved Oxygen	0	0	0	0	0	0
Turbidity	0	0	0	0	0	0
Suspended Solids	0	0	0	0	0	0

10.1.2 No Action Level or Limit Level exceedance was recorded during the reporting period.

Noise Monitoring

10.1.3 No Action Level or Limit Level exceedance was recorded during the reporting period.

10.2 Summary of Environmental Non-Compliance

10.2.1 No environmental non-compliance was recorded in the reporting period.

10.3 Summary of Environmental Complaint

10.3.1 One environmental complaint regarding air quality and one complaint regarding water quality were received during the reporting period. The relevant investigations are conducting by the related parties. The investigation results will be presented when the investigation has been completed.

10.3.2 The Cumulative Complaint Log is presented in **Appendix 10.1**.

10.4 Summary of Environmental Summon and Successful Prosecution

10.4.1 There was no successful environmental prosecution or notification of summons received since the Project commencement. The Cumulative Log for environmental summon and successful prosecution is presented in **Appendix 10.1**.

11 Conclusions and Recommendations

11.1 Conclusion

11.1.1 This 4th Quarterly EM&A Report presents the EM&A works during the reporting period from 1 November 2024 to 31 January 2025 in accordance with the approved Updated EM&A Manual.

11.1.2 Water Quality Monitoring was conducted during the reporting period. No Action or Limit Level exceedance was recorded during the reporting period.

11.1.3 Construction noise monitoring was carried out during the reporting period. No Action Level or Limit Level exceedance was recorded for construction noise monitoring in the reporting period.

11.1.4 Post-translocation monitoring was conducted during the reporting period. None of the translocated individuals from the pre-construction survey was found in the upper and lower receptor sites of Ha Che or the receptor site of Lin Fa Tei during the reporting period. However, 2 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper and Ha Che Lower receptor sites in November 2024. 3 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper and Ha Che Lower receptor sites in December 2024. 2 new individuals of *C. anacoluthon* without markings were captured at the Ha Che Upper receptor sites in January 2025. These individuals, however, were not the translocated individual as their details (i.e., carapace, sex and species) did not match with any of the translocated individuals in the record from November 2024 to January 2025.

11.1.5 Total 13 environmental site inspections and 13 landscape and visual site audits were carried out in the reporting period. Recommendations on mitigation measures were given to the Contractor for remediating the deficiencies identified during the site inspections.

11.1.6 One environmental complaint regarding air quality and one complaint regarding water quality were received during the reporting period. The relevant investigations are conducting by the related parties. The investigation results will be presented when the investigation has been completed.

11.1.7 No notification of summons and successful prosecutions were recorded in the reporting period.

11.1.8 The EM&A methodology has been effective in monitoring the environmental impacts of the Project and the effectiveness of the mitigation measures. The data collected were useful in determining whether the Project had caused unacceptable impacts on the sensitive receivers. Analysis of all EM&A data collected throughout the baseline and the impact monitoring periods demonstrated the environmental acceptability of the Project.

11.2 Comments/ Recommendations

11.2.1 The key environmental mitigation measures for the Project in the coming reporting period expected to be associated with the construction activities include:

Noise

- Only well-maintained plant should be operated on-site, and plant should be maintained regularly during the construction programme; and
- Quality Powered Mechanical Equipment (QPME) should be adopted as far as possible.

Water Quality

- No effluent discharge would be allowed before acquired the effluent discharge license;
- Surface run-off from construction sites should be discharged into dedicated discharge point via adequately designed sand/ silt removal facilities;
- Channels/ earth bunds/ sandbags barriers should be provided on site to properly direct stormwater to silt removal facilities;
- Silt removal facilities, channels and manholes should be maintained, and the deposited silt and grit should be removed regularly;
- Open stockpiles of construction materials on sites should be covered with tarpaulin or similar fabric during rainstorms; and
- Perimeter channels should be provided on site boundaries where necessary to intercept stormwater run-off from outside the site so that it will not wash across the site.

Waste Management

- Provision of sufficient waste disposal points and regular collection of waste;
- Regular cleaning and maintenance programme for drainage system; and
- Chemical containers shall be stored with drip tray underneath.

Ecology

- Minimize loss of habitats and associated wildlife; and
- Using directional lighting to prevent excessive light spill into adjacent natural habitat and disturbance to nocturnal fauna.


Landscape and Visual

- Construction activities shall be carefully designed to minimize impact on existing retained trees; and
- Adequate tree protection measures shall be provided for the trees to be retained on site.

11.2.2 The proposed mitigation measures were properly implemented and were considered effective and efficient in pollution control.

Figures

Figure 1.1 General Site Location Plan

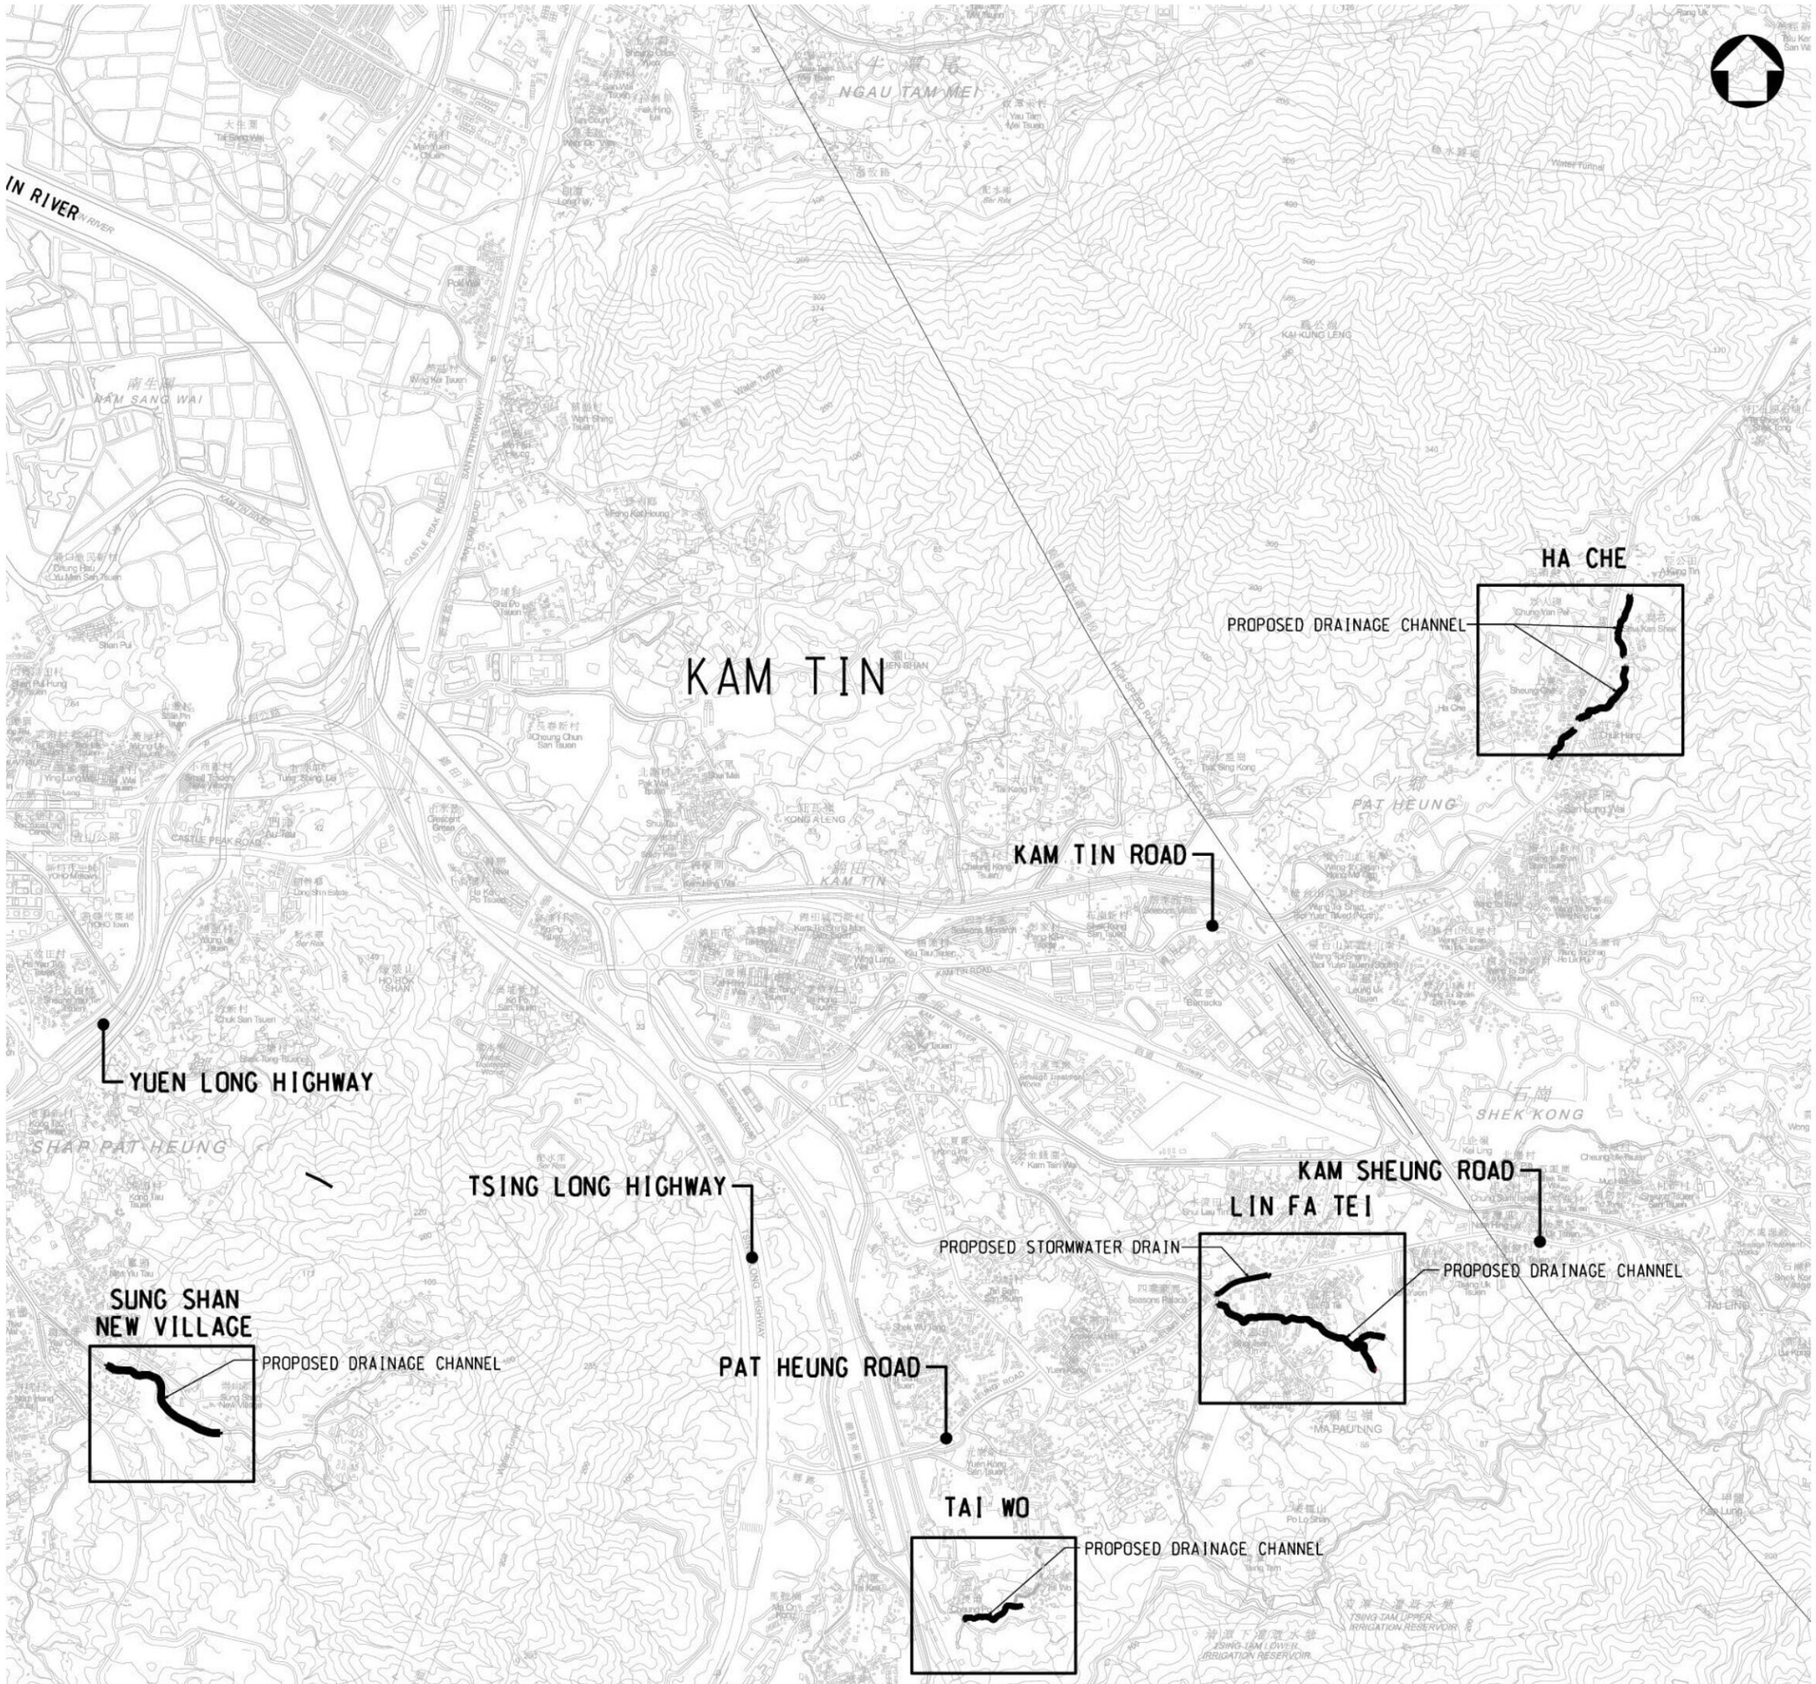

Rev.	Date	Description	By	Chk'd	App'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department

工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
SITE LOCATION PLAN

Scale	Designed	Drawn	Checked	Authorised
N.T.S.	SHC	AC	WCTT	KP
Original Size: A1	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022

Drawing Number: Figure 1.1

Revision: A

Copyright © Atkins Limited (2014)

User name: LEUN3329 Date:07/02/2023 Time: 10:01:16
Filename: P:\CNHK\AGICP\projects\5124336 - CE 22_2013 (DS) Yuen Long-Stage 1\Contract DC/2022\Contract Doc\Volume 3\15-Drawings\General\5124336-TD-C2-GEN-0000_A.dgn

Figure 1.2 Location of Work Areas for the Project

821900 E
822100 E
822300 E
822500 E
831800 N
831600 N
831400 N
SSNV.A
TAI SHU HA ROAD
SHUI TSJU SAN TSUEN
SUNG SHAN NEW VILLAGE
0 10 20 30 40 50 m
1 : 1 000 SCALE BAR

KEY PLAN
N.T.S.

LEGEND:
WORKS BOUNDARY
RECTANGULAR CHANNEL

Rev.	Date	Description	By	Chk'd	App'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability:

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
SUNG SHAN NEW VILLAGE -
GENERAL LAYOUT PLAN

Scale	Designed	Drawn	Checked	Authorised
1 : 1000	SHC	AC	WCTT	KP
Original Size: A1	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022

Drawing Number: Figure 1.2a
Revision:

Copyright © Atkins Limited (2014)

DO NOT SCALE

Millimetres 0 10 100

825500 E

825600 E

825700 E

830800 N

830700 N

CHEUNG PO

TAI WO

大窩


TAI WO

900CU

遊樂場
Playground

教堂
Church

啓業花園
Kai Yip Garden

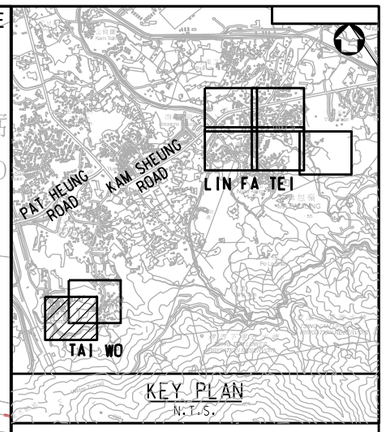

KEY PLAN
N.T.S.

LEGEND:

WORKS BOUNDARY

RECTANGULAR CHANNEL

Rev.	Date	Description	By	Chk'd	Appr'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department

工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
TAI WO -
GENERAL LAYOUT PLAN

Scale	Designed	Drawn	Checked	Authorised
1 : 500	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: **Figure 1.2 b**

Revision: A

0 5 10 15 20 25 m
1 : 500 SCALE BAR

Copyright © Atkins Limited (2014)


DO NOT SCALE

826600 E
826700 E
826800 E
826900 E
827000 E

832200 N
832000 N
831800 N

KAM SHEUNG ROAD
LIN FA TEI
SHUI TSAN TIN
NGAU KENG

Millimetres 0 10 100

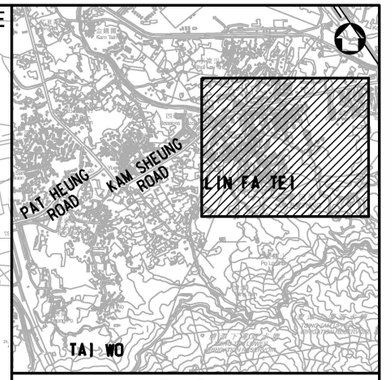

KEY PLAN
N.T.S.

LEGEND:
- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- 450CU — COVERED U-CHANNEL WITH NON-HEAVY DUTY PRECAST CONCRETE COVER
- MANHOLE

Rev.	Date	Description	By	Chk'd	App'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
LIN FA TEI -
GENERAL LAYOUT PLAN

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size: A1	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022

Drawing Number: Figure 1.2 c
Revision:

0 12.5 25 37.5 50 62.5 m
1 : 1 250 SCALE BAR

Copyright © Atkins Limited (2014)

DO NOT SCALE

827700 E


834800 N

834600 N

834400 N

Millimetres 100 0 10

HA CHE

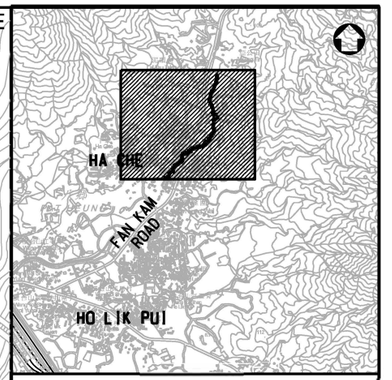

KEY PLAN
N.T.S.

LEGEND:

WORKS BOUNDARY

RECTANGULAR CHANNEL

Rev.	Date	Description	By	Chk'd	Appr'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability:

ATKINS
Member of the SNC-Lavalin Group

Client:
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title:
HA CHE -
GENERAL LAYOUT PLAN

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 1.2 d

Revision:

Copyright © Atkins Limited (2014)

Figure 2.1 Impact Water Quality Monitoring Locations

0 50 100 200 300 400 Meters

C1A

C2

C3A

Legend:

- Work Limit Boundary
- 500 m study area
- Control Station
- Alternative Control Station
- Alternative Impact Station
- Flow direction

Project Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Figure Title:
Water Quality Monitoring Locations at
Sung Shan New Village

Drawn by:	Scale: 1:5,000 on A3	
Checked By:	Date:	
Approved by:		
Figure Number: Figure 2.1a		Revision: R1

DO NOT SCALE

825500 E

825600 E

825700 E

830800 N

830700 N

CHEUNG PO

大嵩

TAI WO

TAI WO

900CU


C5

C4

遊樂場
Playground

教堂
Church

啓業花園
Kai Yip Garden

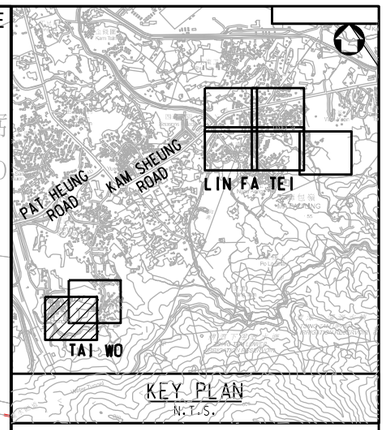

LEGEND:

WORKS BOUNDARY

RECTANGULAR CHANNEL

Control Station

Impact Station

Flow Direction

Rev.	Date	Description	By	Chk'd	Appr'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client: 渠務署 Drainage Services Department

工程管理部
Project Management Division

Contract Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title:
Water Quality Monitoring Locations at Tai Wo

Scale	Designed	Drawn	Checked	Authorised
1 : 500	SHC	AC	WCTT	KP
Original Size: A1	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022

Drawing Number: Figure 2.1b

Revision:

0 5 10 15 20 25 m
1 : 500 SCALE BAR

Copyright © Atkins Limited (2014)

DO NOT SCALE

826800 E 827000 E 827200 E 827400 E 827600 E

832200 N

832000 N

831800 N

831600 N

KAM SHEUNG ROAD

LIN FA TEI

SHUI TSAN TIN


C8

C7A

C6

0 12.5 25 37.5 50 62.5 m
1 : 1,250 SCALE BAR

Millimetres 100 0 10

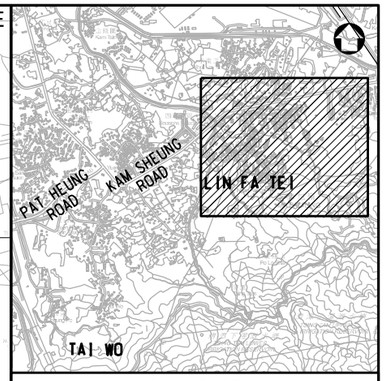

KEY PLAN
N.T.S.

LEGEND:

- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- 450CU — COVERED U-CHANNEL WITH NON-HEAVY DUTY PRECAST CONCRETE COVER
- MANHOLE
- Control Station
- Alternative Control Station
- Impact Station
- Flow Direction

Rev.	Date	Description	By	Chk'd	App'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
Water Quality Monitoring Locations at Lin Fa Tei

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 2.1c

Revision:

Copyright © Atkins Limited (2014)

0 50 100 200 300 400
Meters

C9

C10

LEGEND:

WORKS BOUNDARY

RECTANGULAR CHANNEL

Control Station

Impact Station


Flow Direction


Project Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Figure Title:
Water Quality Monitoring Locations at Ha Che

Drawn by:	Scale: 1:6,500 on A3	
Checked By:	Date:	
Approved by:		
Figure Number: Figure 2.1d		Revision: R1

Figure 3.1 Impact Noise Monitoring Locations

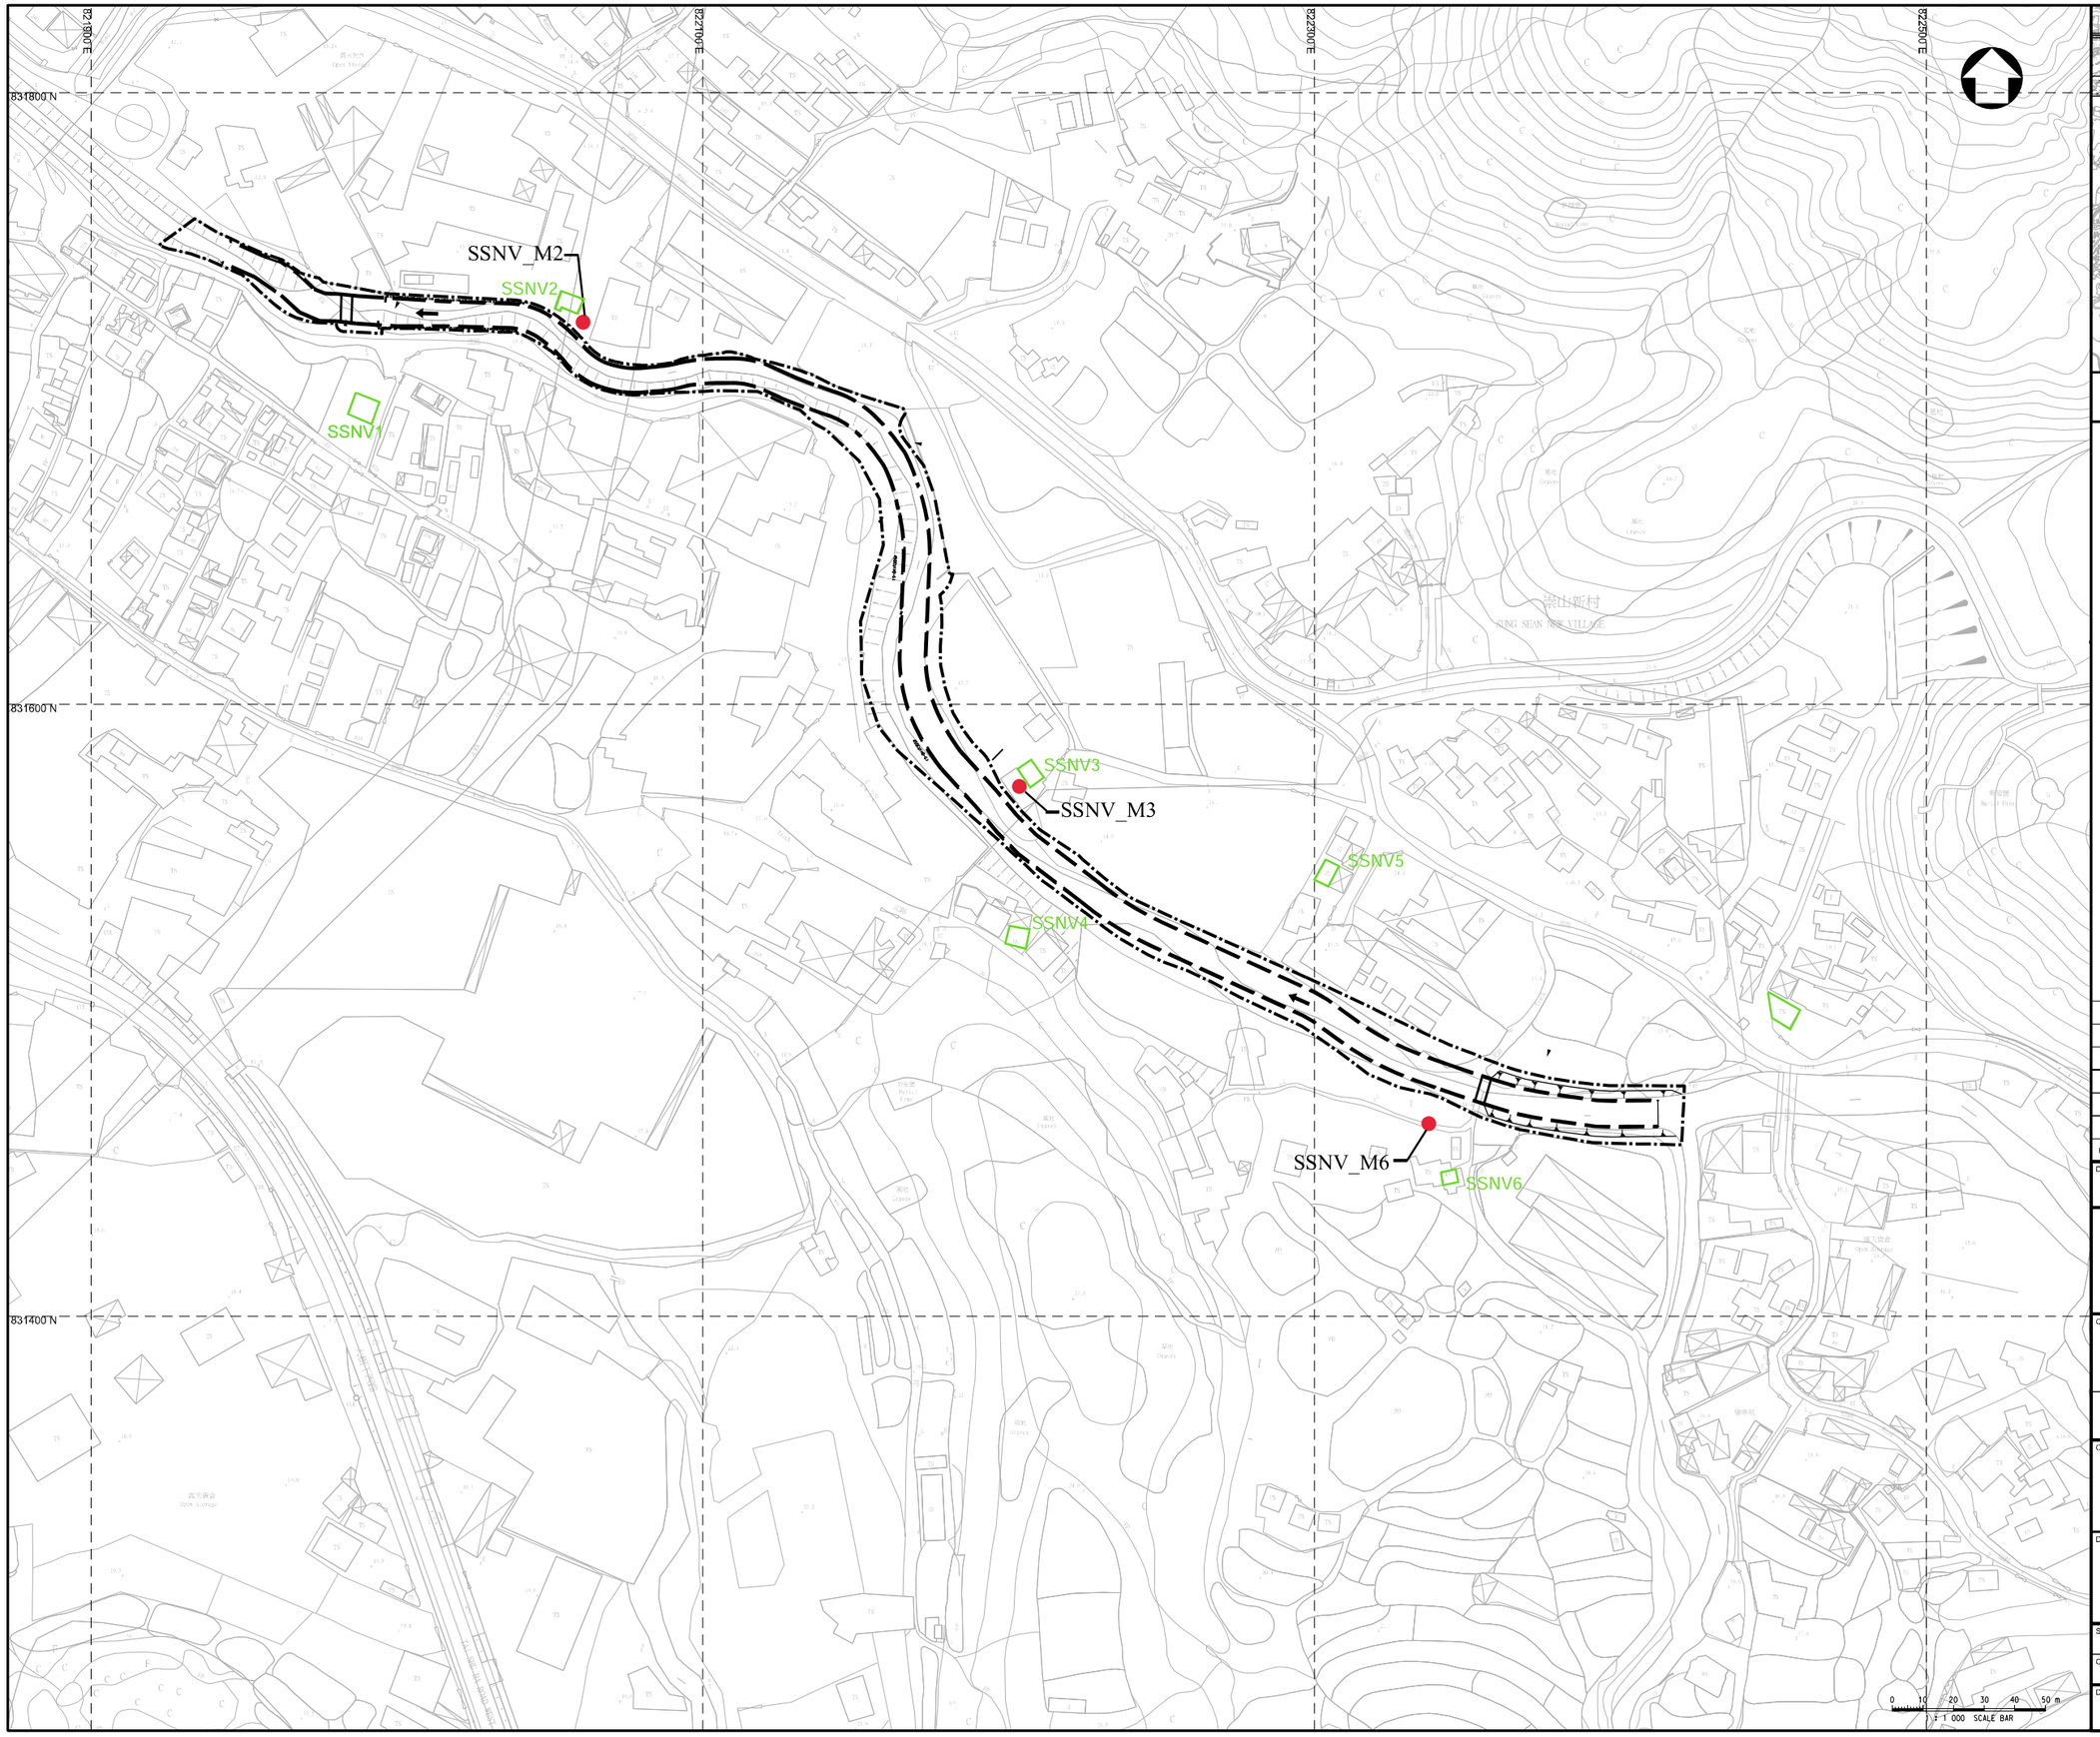

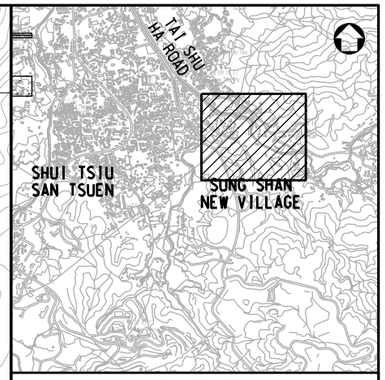

KEY PLAN
N.T.S.

LEGEND:
- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- NOISE SENSITIVE RECEIVER
- NOISE MONITORING STATION

Rev.	Date	Description	By	Chk'd	App'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
Noise Monitoring Locations at
Sung Shan New Village

Scale	Designed	Drawn	Checked	Authorised
1 : 1000	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 3.1a
Revision:

Copyright © Atkins Limited (2014)

DO NOT SCALE

Millimetres 100 0 10

825500 E
825600 E
825700 E
830800 N
830700 N

CHEUNG PO


大嶼
TAI WO

TAI WO

TW_M2
TW_M3
TW1
TW2
TW3

900CU

遊樂場
Playground
教堂
Church
啓業花園
Kai Yip Garden

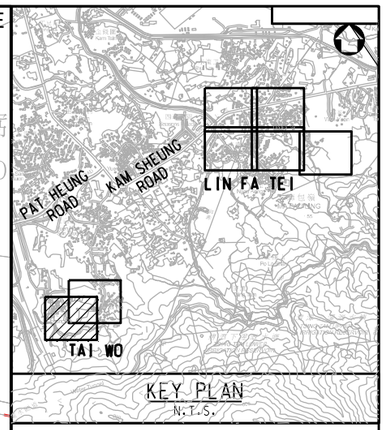

LEGEND:
- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- NOISE SENSITIVE RECEIVER
- NOISE MONITORING STATION

Rev.	Date	Description	By	Chk'd	Appr'd
A	OCT 2022	TENDER ADDENDUM NO.3	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
Noise Monitoring Locations at
Tai Wo

Scale	Designed	Drawn	Checked	Authorised
1 : 500	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 3.1b
Revision: A

0 5 10 15 20 25 m
1 : 500 SCALE BAR

Copyright © Atkins Limited (2014)

DO NOT SCALE

Millimetres 100 0 10

826900 E 827300 E 827700 E 828100 E

832200 N 832000 N 831800 N 831600 N

LFT_M11 KAM SHEUNG ROAD LFT10 LFT11 LFT12 LFT14 LFT13 LFT_M13


LIN FA TEI

LFT9 LFT8 LFT_M7 LFT7 LFT_M5 LFT5 LFT4 LFT_M3A LFT6 LFT_M6 LFT3 LFT_M3

SHUI TSAN TIN

LFT_M1 LFT1 LFT2

0 12.5 25 37.5 50 62.5 m
1 : 250 SCALE BAR

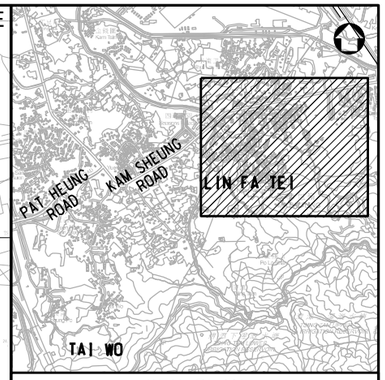

KEY PLAN
N.T.S.

LEGEND:
- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- NOISE SENSITIVE RECEIVER
- NOISE MONITORING STATION
- ALTERNATIVE NOISE MONITORING STATION

Rev.	Date	Description	By	Chk'd	App'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department
工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
Noise Monitoring Locations at
Lin Fa Tei

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 3.1c
Revision:

Copyright © Atkins Limited (2014)

DO NOT SCALE

Millimetres 100 0 10

822700 E

834800 N

834600 N

834400 N

HA CHE

HC_M6

HC8

HC7

HC6

HC_M4

HC_M3

HC5


HC4

HC_M3A

HC3

HC2

HC1

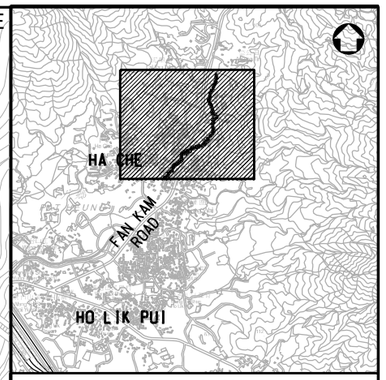

KEY PLAN
N.T.S.

LEGEND:

- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- NOISE SENSITIVE RECEIVER
- NOISE MONITORING STATION
- ALTERNATIVE NOISE MONITORING STATION

Rev.	Date	Description	By	Chk'd	App'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client: 渠務署 Drainage Services Department

工程管理部
Project Management Division

Contract Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title:
Noise Monitoring Locations at
Ha Che

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 3.1d

Revision:

Copyright © Atkins Limited (2014)

Figure 8.1 Area for Archaeological Survey

DO NOT SCALE


826600 E
826700 E
826800 E
826900 E
827000 E

832200 N
832000 N
831800 N

KAM SHEUNG ROAD
LIN FA TEI
SHUI TSAN TIN
NGAU KENG

Millimetres 0 10 100

0 12.5 25 37.5 50 62.5 m
1 : 1 250 SCALE BAR

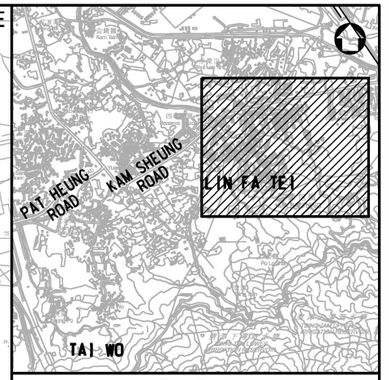

KEY PLAN
N.T.S.

LEGEND:

- WORKS BOUNDARY
- RECTANGULAR CHANNEL
- 450CU — COVERED U-CHANNEL WITH NON-HEAVY DUTY PRECAST CONCRETE COVER
- MANHOLE
- AREA IDENTIFIED FOR ARCHAEOLOGICAL SURVEY

Rev.	Date	Description	By	Chk'd	App'd
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT
Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client
渠務署
Drainage Services Department

工程管理部
Project Management Division

Contract Title
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title
AREA IDENTIFIED FOR ARCHAEOLOGICAL SURVEY

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size: A1	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022	Date: JUL 2022

Drawing Number: Figure 8.1
Revision:

Copyright © Atkins Limited (2014)

Figure 8.2 Layout plan showing distance between the works area at Ha Che and the Lan Fong Study Hall

DO NOT SCALE

827700 E

834800 N

834600 N

834400 N

HA CHE

A KUNG TIN

SHEUNG CHE TSUEN


CHUK HANG

395.34 m

63.76 m

Lan Fong Study Hall

Millimetres 0 10 100

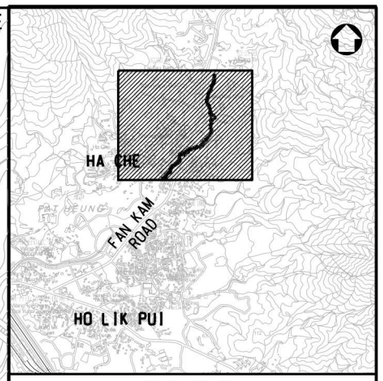

KEY PLAN
N.T.S.

NOTES:

1. FOR GENERAL LAYOUT PLAN, REFER TO DRAWING NO. 5124336-TD-C2-GEN-0000.
2. FOR GENERAL NOTES, REFER TO DRAWING NOS. 5124336-TD-C2-GEN-0001 & 0002.
3. FOR LEGENDS, REFER TO DRAWING NO. 5124336-TD-C2-GEN-0003.
4. FOR PROPOSED ALIGNMENT, REFER TO DRAWING NOS. 5124336-TD-C2-GEN-8001 TO 8004.

Works area

CONTROLLED COPY

Rev.	Date	Description	By	Chk'd	App'd
			SAH	M	KP
A	NOV 2022	TENDER ADDENDUM NO. 4	SHC	WCTT	KP
-	JUL 2022	ISSUE FOR TENDER	SHC	WCTT	KP

Drawing Status: CONTRACT

Suitability: -

ATKINS
Member of the SNC-Lavalin Group

Client: 渠務署 Drainage Services Department

工程管理部
Project Management Division

Contract Title:
CONTRACT NO. DC/2022/02
DRAINAGE IMPROVEMENT WORKS
AT YUEN LONG -
STAGE 2

Drawing Title:
HA CHE -
GENERAL LAYOUT PLAN

Scale	Designed	Drawn	Checked	Authorised
1 : 1250	SHC	AC	WCTT	KP
Original Size	Date	Date	Date	Date
A1	JUL 2022	JUL 2022	JUL 2022	JUL 2022

Drawing Number: Figure 8.2

Revision: A

Copyright © Atkins Limited (2014)


User name: LEUN3329 Date:08/02/2023 Time:17:24:16
Filename: P:\CNHKA\GIS\Project\5124336 - CE 22_2013 (DS) Yuen Long-Stage 1\Contract DC2022\02\Contract Doc\Volume 3\15-Drawings\dgn\HC\5124336-TD-C2-GEN-8000_A.dgn

Appendices

Appendix 1.1 Construction Programme

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
1	*Starting date*	#########	Earlier Than	1 day	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	0 days		
2	*Access date*	NA	As Possible	270 days	Mon 23/5/29	Fri 24/2/23	Mon 23/5/29	Fri 24/2/23	Tue 26/7/7	Fri 27/4/2	1134 days		
3	Portion A	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Tue 26/7/7	Fri 27/4/2	1134 days		1
4	Portion B	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	Sat 26/9/5	Fri 27/4/2	1194 days		1
5	Portion C1 & C2	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Tue 26/7/7	Fri 27/4/2	1134 days		1
6	Portion C3	NA	As Possible	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Fri 27/4/2	Fri 27/4/2	1404 days		1
7	Portion D	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	Sat 26/9/5	Fri 27/4/2	1194 days		1
8	Portion E1	NA	As Possible	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Fri 27/4/2	Fri 27/4/2	1404 days		1
9	Portion E2	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Tue 26/7/7	Fri 27/4/2	1134 days		1
10	*Completion Date*	NA	As Possible	1155 days	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	0 days		
11	Section I - Drainage Improvement Works at Sung Shan New Village	Thu 26/5/28	Later Than	1095 days	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	0 days		1
12	Section II - Drainage Improvement Works at Tai Wo	Tue 25/8/26	Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days		1
13	Section III - Drainage Improvement Works at Lin Fa Tei (except flood wall construction and drainage improvement works along Kam Sheung Road)	Mon 26/7/27	Finish No Later Than	1155 days	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	0 days		1
14	Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)	Thu 26/5/28	Finish No Later Than	1095 days	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	0 days		1
15	Section V - Drainage Improvement Works at Shan Ha Tsuen	#########	Later Than	973 days	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	0 days		1
16	Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tei	Tue 25/8/26	Finish No Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days		1
17	Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Chainage 626.224m - 678.859m) at Ha Che	Tue 25/8/26	Finish No Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days		1
39	Planned Completion Day of whole of the works	NA	As Possible	584 days	Tue 25/8/26	Fri 27/4/2	Tue 25/8/26	Fri 27/4/2	Wed 25/8/27	Fri 27/4/2	0 days		
40	**Section I - Drainage Improvement Works at Sung Shan New Village**	NA	As Possible	309 days	Fri 26/5/29	Fri 27/4/2	Fri 26/5/29	Fri 27/4/2	Fri 26/5/29	Fri 27/4/2	0 days		
41	EOT - Inclement weather (anticipated upto 31 Jul 2024)	Thu 26/8/6	Later Than	70 days	Fri 26/5/29	Thu 26/8/6	Fri 26/5/29	Thu 26/8/6	Fri 26/5/29	Thu 26/8/6	0 days		11
42	EOT - Uncharted/Retained Trees obstructing the works	Fri 26/12/4	Earlier Than	120 days	Fri 26/12/4	Fri 27/4/2	Fri 26/12/4	Fri 27/4/2	Fri 26/12/4	Fri 27/4/2	0 days		41
43	**Section II - Drainage Improvement Works at Tai Wo**	NA	As Possible	251 days	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	0 days		
44	EOT - Blockade of access by others	Mon 26/5/4	Later Than	251 days	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	0 days		12
45	**Section III - Drainage Improvement Works at Lin Fa Tei (except flood wall construction and drainage improvement works along Kam Sheung Road)**	NA	As Soon As Possible	70 days	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	0 days		
46	EOT - Inclement weather (anticipated upto 31 Jul 2024)	#########	Later Than	70 days	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	0 days		13
47	**Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)**	NA	As Soon As Possible	130 days	Fri 26/5/29	Mon 26/10/5	Fri 26/5/29	Mon 26/10/5	Fri 26/5/29	Mon 26/10/5	0 days		
48	EOT - Inclement weather (anticipated upto 31 Jul 2024)	Thu 26/8/6	Later Than	70 days	Fri 26/5/29	Thu 26/8/6	Fri 26/5/29	Thu 26/8/6	Fri 26/5/29	Thu 26/8/6	0 days		14
49	EOT - Additional request from landlord of HC06,07	#########	Later Than	60 days	Fri 26/8/7	Mon 26/10/5	Fri 26/8/7	Mon 26/10/5	Fri 26/8/7	Mon 26/10/5	0 days		48
50	**Section V - Drainage Improvement Works at Shan Ha Tsuen**	NA	As Possible	70 days	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	0 days		
51	EOT - Inclement weather (anticipated upto 31 Jul 2024)	Mon 26/4/6	Later Than	70 days	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	0 days		15
52	**Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tei**	NA	As Soon As Possible	240 days	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	0 days		
53	EOT - Difficulty/infeasibility for construction of 1650mm dia. pipe at Kam Sheur	Thu 26/4/23	Later Than	240 days	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	0 days		16
54	**Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Chainage 626.224m - 678.859m) at Ha Che**	NA	As Soon As Possible	0 days	Tue 25/8/26	Tue 25/8/26	Tue 25/8/26	Tue 25/8/26	Fri 27/4/2	Fri 27/4/2	584 days		17
55													
56	Project establishment	NA	As Possible	307 days	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Fri 27/4/2	0 days		
57	**Project Manager's Accommodation**	NA	As Possible	209 days	Mon 23/8/21	Sat 24/3/16	Mon 23/8/21	Sat 24/3/16	Thu 26/9/17	Fri 27/4/2	1112 days		1FS-1 day
58	PM1001 - Possession of Works Area at 22 Fan Kam road [A]	Fri 23/9/1	Earlier Than	1 day	Fri 23/9/1	Fri 23/9/1	Fri 23/9/1	Fri 23/9/1	Thu 26/9/17	Thu 26/9/17	1112 days	0	
59	**Rennovation and Certification of ex. PM accommodation**	NA	As Possible	197 days	Sat 23/9/2	Sat 24/3/16	Sat 23/9/2	Sat 24/3/16	Fri 26/9/18	Fri 27/4/2	1112 days	0	
60	Inspection and review of ex. PM accommodation [A]	NA	As Possible	100 days	Sat 23/9/2	Sun 23/12/10	Sat 23/9/2	Sun 23/12/10	Fri 26/9/18	Sat 26/12/26	1112 days		58
61	Arranging time slot with RSS for power and server down [A]	NA	As Possible	83 days	Mon 23/12/11	Sat 24/3/2	Mon 23/12/11	Sat 24/3/2	Sun 26/12/27	Fri 27/3/19	1112 days	0	60
62	Issuance of check certificates [A]	NA	As Possible	14 days	Sun 24/3/3	Sat 24/3/16	Sun 24/3/3	Sat 24/3/16	Sat 27/3/20	Fri 27/4/2	1112 days	0	61
63	C11 Tendering procedure for EDMS & DWSS [A]	#########	Earlier Than	30 days	Mon 23/8/21	Tue 23/9/19	Mon 23/8/21	Tue 23/9/19	Sat 27/1/23	Sun 27/2/21	1251 days	0	
64	Installation and commissioning of EDMS & DWSS [A]	NA	As Possible	40 days	Wed 23/9/20	Sun 23/10/29	Wed 23/9/20	Sun 23/10/29	Mon 27/2/22	Fri 27/4/2	1251 days	0	63
65	**Environmental Team (ET) procurement**	NA	As Possible	190 days	Tue 23/8/15	Tue 24/2/20	Tue 23/8/15	Tue 24/2/20	Wed 23/8/30	Fri 27/4/2	15 days		
66	C9 Tendering procedure [A]	Tue 23/8/15	Earlier Than	58 days	Tue 23/8/15	Wed 23/10/11	Tue 23/8/15	Wed 23/10/11	Wed 23/8/30	Thu 23/10/26	15 days	0	
67	Commencement for ET (Aurecon) [A]	NA	As Possible	1 day	Thu 23/10/12	Thu 23/10/12	Thu 23/10/12	Thu 23/10/12	Fri 23/10/27	Fri 23/10/27	15 days	0	66
68	Proposal and Acceptance of ET Members [A]	NA	As Possible	18 days	Fri 23/10/13	Mon 23/10/30	Fri 23/10/13	Mon 23/10/30	Sat 23/10/28	Tue 23/11/14	15 days	0	67
69	Updating and Acceptance of EM&A Manual [A]	NA	As Possible	23 days	Tue 23/10/31	Wed 23/11/22	Tue 23/10/31	Wed 23/11/22	Wed 23/11/15	Thu 23/12/7	15 days	0	68
70	Notice of Commencement of Construction to EPD [A]	NA	As Possible	90 days	Thu 23/11/23	Tue 24/2/20	Thu 23/11/23	Tue 24/2/20	Fri 23/12/8	Wed 24/3/6	15 days	0	69
71	Complete necessary submissions to EPD [A]	NA	As Possible	20 days	Thu 24/2/1	Tue 24/2/20	Thu 24/2/1	Tue 24/2/20	Sun 27/3/14	Fri 27/4/2	1137 days	0	70FF
76	**Setup Public Liaison Team**	NA	As Possible	120 days	Mon 23/5/15	Mon 23/9/11	Mon 23/5/15	Mon 23/9/11	Mon 23/5/15	Mon 23/9/11	0 days		
77	Recruitment of Public Liaison Officer [A]	NA	As Possible	90 days	Mon 23/5/15	Sat 23/8/12	Mon 23/5/15	Sat 23/8/12	Mon 23/5/15	Sat 23/8/12	0 days	0	
78	Appointment and Acceptance of Public Liaison Officer [A]	NA	As Possible	30 days	Sun 23/8/13	Mon 23/9/11	Sun 23/8/13	Mon 23/9/11	Sun 23/8/13	Mon 23/9/11	0 days	0	77
86	**Works Area establishment**	NA	As Possible	44 days	Fri 23/9/1	Sat 23/10/14	Fri 23/9/1	Sat 23/10/14	Sat 23/9/16	Fri 27/4/2	15 days		
87	PM1001 - Possession of Works Area at 22 Fan Kam road [A]	Fri 23/9/1	Earlier Than	1 day	Fri 23/9/1	Fri 23/9/1	Fri 23/9/1	Fri 23/9/1	Sat 23/9/16	Sat 23/9/16	15 days	0	
88	Establish concrete haul road and slab [A]	NA	As Possible	43 days	Sat 23/9/2	Sat 23/10/14	Sat 23/9/2	Sat 23/10/14	Fri 27/2/19	Fri 27/4/2	1266 days	0	87
89	**Contractor's Accommodation (office and welfare facilities)**	NA	As Possible	145 days	Sat 23/9/2	Wed 24/1/24	Sat 23/9/2	Wed 24/1/24	Sun 23/9/17	Fri 27/4/2	15 days		
90	Establish temporary site office (containers) [A]	NA	As Possible	24 days	Sat 23/9/2	Mon 23/9/25	Sat 23/9/2	Mon 23/9/25	Sun 23/9/17	Tue 23/10/10	15 days	0	87
98	C9 Tendering procedure for Contractor's Site Office [A]	NA	As Possible	28 days	Sat 23/9/2	Fri 23/9/29	Sat 23/9/2	Fri 23/9/29	Mon 26/11/9	Sun 26/12/6	1164 days	0	87
99	Proposal and Acceptance of Temp. Works Design and Method Statement [A]	NA	As Possible	35 days	Sat 23/9/30	Fri 23/11/3	Sat 23/9/30	Fri 23/11/3	Mon 26/12/7	Sun 27/1/10	1164 days	0	98
100	Construction of Footing [A]	NA	As Possible	15 days	Sat 23/11/4	Sat 23/11/18	Sat 23/11/4	Sat 23/11/18	Mon 27/1/11	Mon 27/1/25	1164 days	0	99
101	Construction of Structure [A]	NA	As Possible	45 days	Sun 23/11/19	Tue 24/1/2	Sun 23/11/19	Tue 24/1/2	Tue 27/1/26	Thu 27/3/11	1164 days	0	100
102	Interior furnishment and Furnitures [A]	NA	As Possible	15 days	Wed 24/1/3	Wed 24/1/17	Wed 24/1/3	Wed 24/1/17	Fri 27/3/12	Fri 27/3/26	1164 days	0	101
103	Move-in [A]	NA	As Possible	7 days	Thu 24/1/18	Wed 24/1/24	Thu 24/1/18	Wed 24/1/24	Sat 27/3/27	Fri 27/4/2	1164 days	0	102
104													
105	Section I	NA	As Possible	1285 days	Tue 23/5/30	Fri 26/12/4	Tue 23/5/30	Fri 26/12/4	Tue 23/5/30	Fri 27/4/2	0 days		
2	access date of Portion A	Fri 24/2/23	Later Than	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	0 days	0	\\WingTatNasC
3	Period of section I (Sung Shan New Village)	#########	Later Than	1095 days	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Wed 23/5/31	1 day	0	\\WingTatNasC
4	Planned Completion Day	Fri 26/12/4	Later Than	189 days	Fri 26/5/29	Thu 26/12/3	Fri 26/5/29	Thu 26/12/3	Sat 26/5/30	Fri 26/12/4	1 day	0	3
5	Early access (partial) [A]	NA	As Possible	200 days	Tue 23/5/30	Fri 23/12/15	Tue 23/5/30	Fri 23/12/15	Tue 23/8/8	Fri 24/2/23	70 days	0	\\WingTatNasC
6	**Site Establishment**	NA	As Possible	878 days	Tue 23/9/12	Thu 26/2/5	Tue 23/9/12	Thu 26/2/5	Tue 23/9/12	Fri 27/4/2	0 days		
7	Prepare and Accept Temp. Works Design and Method Statement	NA	As Possible	864 days	Tue 23/9/26	Thu 26/2/5	Tue 23/9/26	Thu 26/2/5	Wed 24/2/28	Fri 26/7/10	155 days	0	\\WingTatNasC
8	Public Liaison and Negotiation with Village Rep.	NA	As Possible	164 days	Tue 23/9/12	Thu 24/2/22	Tue 23/9/12	Thu 24/2/22	Tue 23/9/12	Thu 24/2/22	0 days	0	\\WingTatNasC
9	Initial Survey	NA	As Possible	714 days	Fri 24/2/23	Thu 26/2/5	Fri 24/2/23	Thu 26/2/5	Sat 24/7/27	Fri 26/7/10	155 days	0	8,5FS-1 day
10	Initial Safety & Environmental measures [A]	NA	As Possible	21 days	Fri 24/2/23	Thu 24/3/14	Fri 24/2/23	Thu 24/3/14	Fri 24/2/23	Thu 24/3/14	0 days	0	8,5FS-1 day
13	Setup of instrumentation and monitoring [A]	Fri 26/12/4	Later Than	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Sat 26/11/7	Fri 26/12/4	967 days	0	10

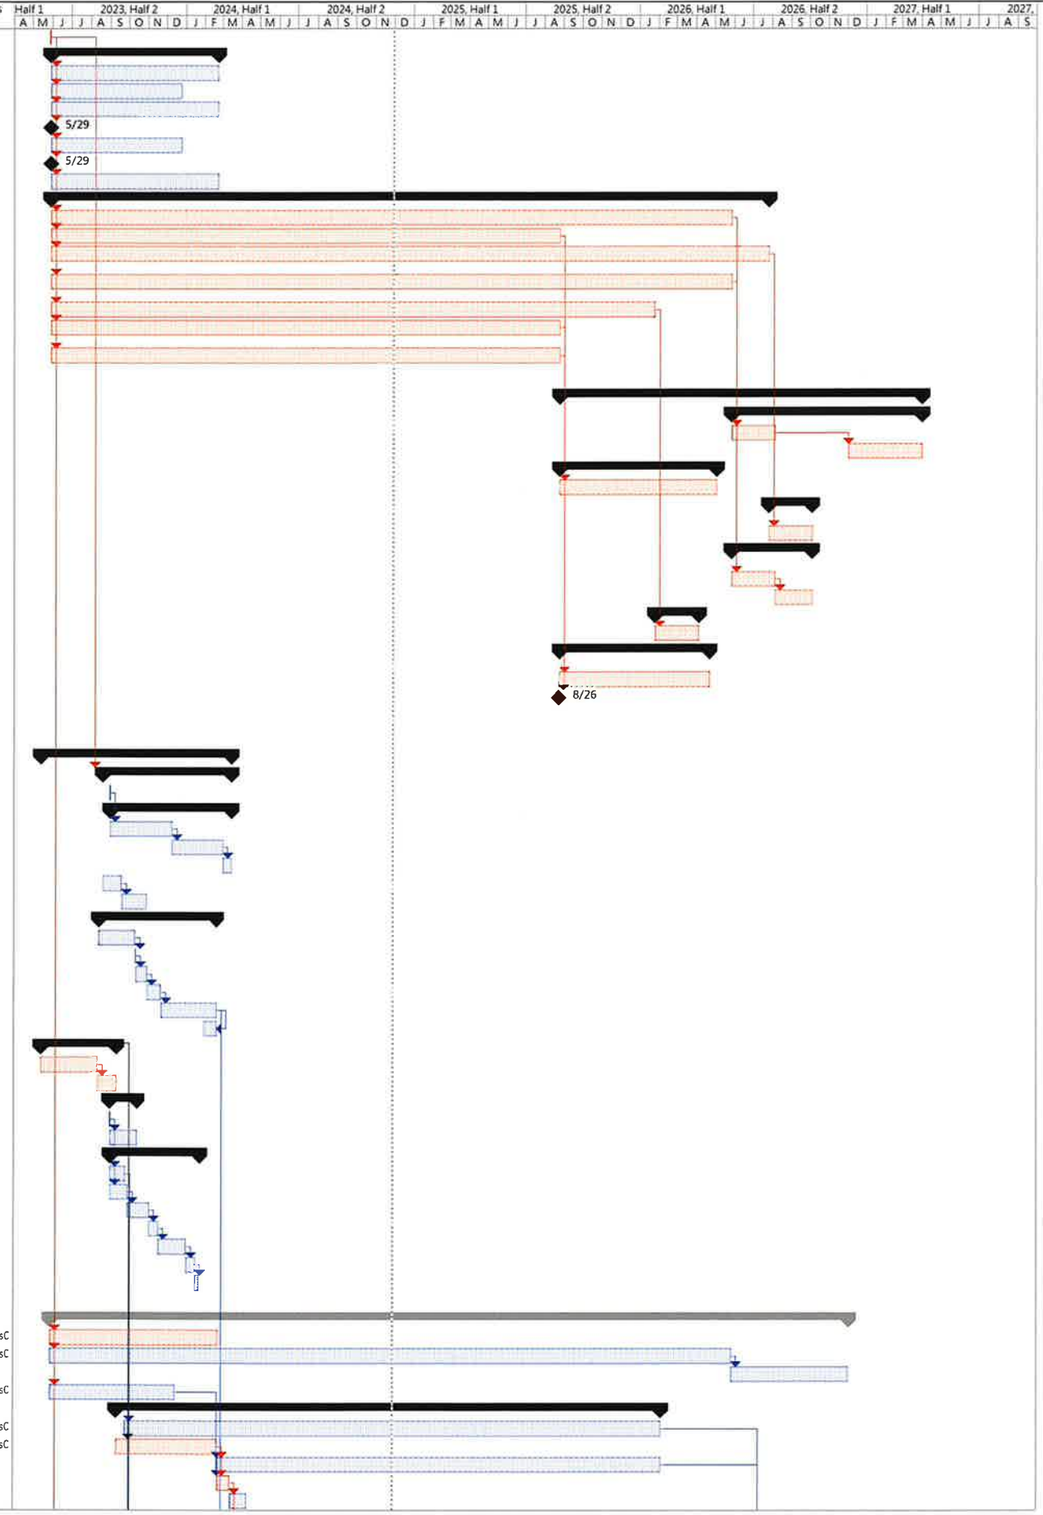


Revision.: 14.0 Date: 31 October 2024

Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
15	EIAO Commencement of Construction [A]	NA	As Possible	1 day	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Fri 26/12/4	Fri 26/12/4	1017 days	0	\\WingTatNasC
16	Environmental Baseline Monitoring [A]	NA	As Possible	28 days	Tue 24/1/23	Mon 24/2/19	Tue 24/1/23	Mon 24/2/19	Sat 27/3/6	Fri 27/4/2	1138 days	0	15FS-30 days
17	Condition Survey [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	10
18	Vegetation Survey [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	10
19	Tree Survey [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	10
20	Site Clearance [A]	NA	As Possible	60 days	Fri 24/4/12	Mon 24/6/10	Fri 24/4/12	Mon 24/6/10	Fri 24/4/12	Mon 24/6/10	0 days	0	17,18,19
21	[PMIxxx] TPRP for Additional Trees (impact to be ascertained)	NA	As Possible	90 days	Sun 24/5/12	Fri 24/8/9	Sun 24/5/12	Fri 24/8/9	Sun 24/5/12	Fri 24/8/9	0 days	0	20FS-30 days
22	[PMI-xxx] Aquilaria Sinensis seedling (impact to be ascertained)	Fri 26/12/4	Later Than	60 days	Sun 24/5/12	Wed 24/7/10	Sun 24/5/12	Wed 24/7/10	Tue 26/10/6	Fri 26/12/4	877 days	0	20FS-30 days
23	UU detection	NA	As Possible	30 days	Sun 24/5/12	Mon 24/6/10	Sun 24/5/12	Mon 24/6/10	Tue 24/6/11	Wed 24/7/10	30 days	0	20FS-30 days
24	Establish access(es) to channels [A]	NA	As Possible	30 days	Sun 24/5/12	Mon 24/6/10	Sun 24/5/12	Mon 24/6/10	Tue 24/6/11	Wed 24/7/10	30 days	0	20FS-30 days
25	Guarding / Barrier / Hoarding [A]	NA	As Possible	30 days	Tue 24/6/11	Wed 24/7/10	Tue 24/6/11	Wed 24/7/10	Thu 24/7/11	Fri 24/8/9	30 days	0	24,23
26	**Drainage Channels Works**	**NA**	**As Possible**	**847 days**	**Sat 24/8/10**	**Fri 26/12/4**	**Sat 24/8/10**	**Fri 26/12/4**	**Sat 24/8/10**	**Fri 26/12/4**	**0 days**		
27	Excavate & Backfill ex. Unregistered feature [A]	NA	As Possible	20 days	Sat 24/8/10	Thu 24/8/29	Sat 24/8/10	Thu 24/8/29	Sat 24/8/10	Thu 24/8/29	0 days	0	25,21
28	Relocate/Divert ex. Utilities [A]	NA	As Possible	20 days	Sat 24/8/10	Thu 24/8/29	Sat 24/8/10	Thu 24/8/29	Sat 24/8/10	Thu 24/8/29	0 days	0	25,21
29	Demolish & relocate metal frame YLL796/B/9 [A]	NA	As Possible	30 days	Fri 24/8/30	Sat 24/9/28	Fri 24/8/30	Sat 24/9/28	Fri 24/8/30	Sat 24/9/28	0 days	0	27,28
30	[PMI-017] Uncharted/Additional Trees obstructing the works (impact to be ascertained]	NA	As Soon As Possible	60 days	Sun 24/9/29	Wed 24/11/27	Sun 24/9/29	Wed 24/11/27	Sun 24/9/29	Wed 24/11/27	0 days	0	29
31	**SSNV04 CH.A300.00~CH.A400.00**	**NA**	**As Possible**	**86 days**	**Thu 24/11/28**	**Fri 25/2/21**	**Thu 24/11/28**	**Fri 25/2/21**	**Thu 24/11/28**	**Fri 25/2/21**	**0 days**		
32	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	50 days	Thu 24/11/28	Thu 25/1/16	Thu 24/11/28	Thu 25/1/16	Thu 24/11/28	Thu 25/1/16	0 days	2	30
33	Excavation and Lateral Support	NA	As Possible	50 days	Thu 24/12/12	Thu 25/1/30	Thu 24/12/12	Thu 25/1/30	Thu 24/12/12	Thu 25/1/30	0 days	2	32FS-36 days
34	**Ground and Edge Beams**	**NA**	**As Possible**	**30 days**	**Thu 24/12/26**	**Fri 25/1/24**	**Thu 24/12/26**	**Fri 25/1/24**	**Thu 24/12/26**	**Fri 25/1/24**	**0 days**		
35	Rebar Fixing	NA	As Possible	20 days	Thu 24/12/26	Tue 25/1/14	Thu 24/12/26	Tue 25/1/14	Thu 24/12/26	Tue 25/1/14	0 days	1	33FS-36 days
36	Formwork Erection and Cast-in items	NA	As Possible	20 days	Sun 25/1/5	Fri 25/1/24	Sun 25/1/5	Fri 25/1/24	Sun 25/1/5	Fri 25/1/24	0 days	1	35FS-10 days
37	Concreting	NA	As Possible	4 days	Wed 25/1/15	Sat 25/1/18	Wed 25/1/15	Sat 25/1/18	Wed 25/1/15	Sat 25/1/18	0 days	0	36FS-10 days
38	**Walls**	**NA**	**As Possible**	**30 days**	**Sun 25/1/19**	**Mon 25/2/17**	**Sun 25/1/19**	**Mon 25/2/17**	**Sun 25/1/19**	**Mon 25/2/17**	**0 days**		
39	Rebar Fixing	NA	As Possible	20 days	Sun 25/1/19	Fri 25/2/7	Sun 25/1/19	Fri 25/2/7	Sun 25/1/19	Fri 25/2/7	0 days	1	37
40	Formwork Erection and Cast-in items	NA	As Possible	20 days	Wed 25/1/29	Mon 25/2/17	Wed 25/1/29	Mon 25/2/17	Wed 25/1/29	Mon 25/2/17	0 days	1	39FS-10 days
41	Concreting	NA	As Possible	4 days	Sat 25/2/8	Tue 25/2/11	Sat 25/2/8	Tue 25/2/11	Sat 25/2/8	Tue 25/2/11	0 days	0	40FS-10 days
42	Backfilling and Compaction	NA	As Possible	10 days	Wed 25/2/12	Fri 25/2/21	Wed 25/2/12	Fri 25/2/21	Wed 25/2/12	Fri 25/2/21	0 days	0	41
43	Removal of Sheetpiles	NA	As Possible	10 days	Wed 25/2/12	Fri 25/2/21	Wed 25/2/12	Fri 25/2/21	Wed 25/2/12	Fri 25/2/21	0 days	0	42FS-10 days
44	**SSNV03 CH.A400.00~CH.A500.00**	**NA**	**As Possible**	**102 days**	**Sat 25/2/22**	**Tue 25/6/3**	**Sat 25/2/22**	**Tue 25/6/3**	**Sat 25/2/22**	**Tue 25/6/3**	**0 days**		
45	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	48 days	Sat 25/2/22	Thu 25/4/10	Sat 25/2/22	Thu 25/4/10	Sat 25/2/22	Thu 25/4/10	0 days	2	43
46	Excavation and Lateral Support	NA	As Possible	48 days	Thu 25/3/6	Tue 25/4/22	Thu 25/3/6	Tue 25/4/22	Thu 25/3/6	Tue 25/4/22	0 days	2	45FS-36 days
47	**Ground and Edge Beams**	**NA**	**As Possible**	**30 days**	**Tue 25/3/18**	**Wed 25/4/16**	**Tue 25/3/18**	**Wed 25/4/16**	**Tue 25/3/18**	**Wed 25/4/16**	**0 days**		
48	Rebar Fixing	NA	As Possible	20 days	Tue 25/3/18	Sun 25/4/6	Tue 25/3/18	Sun 25/4/6	Tue 25/3/18	Sun 25/4/6	0 days	1	46FS-36 days
49	Formwork Erection and Cast-in items	NA	As Possible	20 days	Fri 25/3/28	Wed 25/4/16	Fri 25/3/28	Wed 25/4/16	Fri 25/3/28	Wed 25/4/16	0 days	1	48FS-10 days
50	Concreting	NA	As Possible	4 days	Mon 25/4/7	Thu 25/4/10	Mon 25/4/7	Thu 25/4/10	Mon 25/4/7	Thu 25/4/10	0 days	0	49FS-10 days
51	**Walls**	**NA**	**As Possible**	**30 days**	**Fri 25/4/11**	**Sat 25/5/10**	**Fri 25/4/11**	**Sat 25/5/10**	**Fri 25/4/11**	**Sat 25/5/10**	**0 days**		
52	Rebar Fixing	NA	As Possible	20 days	Fri 25/4/11	Wed 25/4/30	Fri 25/4/11	Wed 25/4/30	Fri 25/4/11	Wed 25/4/30	0 days	1	50
53	Formwork Erection and Cast-in items	NA	As Possible	20 days	Mon 25/4/21	Sat 25/5/10	Mon 25/4/21	Sat 25/5/10	Mon 25/4/21	Sat 25/5/10	0 days	1	52FS-10 days
54	Concreting	NA	As Possible	4 days	Thu 25/5/1	Sun 25/5/4	Thu 25/5/1	Sun 25/5/4	Thu 25/5/1	Sun 25/5/4	0 days	0	53FS-10 days
55	Backfilling and Compaction	NA	As Possible	20 days	Mon 25/5/5	Sat 25/5/24	Mon 25/5/5	Sat 25/5/24	Mon 25/5/5	Sat 25/5/24	0 days	0	54
56	Removal of Sheetpiles	NA	As Possible	20 days	Thu 25/5/15	Tue 25/6/3	Thu 25/5/15	Tue 25/6/3	Thu 25/5/15	Tue 25/6/3	0 days	0	55FS-10 days
57	1:2 slope works	Fri 26/12/4	Later Than	35 days	Wed 25/6/4	Tue 25/7/8	Wed 25/6/4	Tue 25/7/8	Sat 26/10/31	Fri 26/12/4	514 days	5	56
58	Demolish & relocate wall, hoarding YLL796/B/13,13B	NA	As Possible	14 days	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	0 days	0	56FS-10 days
59	Demolish & relocate OSC YLL796/B/14A,14B	NA	As Possible	14 days	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	0 days	0	56FS-10 days
60	Demolish & relocate fence & wall YLL796/B/14	NA	As Possible	14 days	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	Sun 25/5/25	Sat 25/6/7	0 days	0	56FS-10 days
61	**SSNV05 CH.A200.00~CH.A300.00**	**NA**	**As Possible**	**98 days**	**Sun 25/6/8**	**Sat 25/9/13**	**Sun 25/6/8**	**Sat 25/9/13**	**Sun 25/6/8**	**Sat 25/9/13**	**0 days**		
62	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	48 days	Sun 25/6/8	Fri 25/7/25	Sun 25/6/8	Fri 25/7/25	Sun 25/6/8	Fri 25/7/25	0 days	2	58,59,60
63	Excavation and Lateral Support	NA	As Possible	48 days	Fri 25/6/20	Wed 25/8/6	Fri 25/6/20	Wed 25/8/6	Fri 25/6/20	Wed 25/8/6	0 days	2	62FS-36 days
64	**Ground and Edge Beams**	**NA**	**As Possible**	**28 days**	**Wed 25/7/2**	**Tue 25/7/29**	**Wed 25/7/2**	**Tue 25/7/29**	**Wed 25/7/2**	**Tue 25/7/29**	**0 days**		
65	Rebar Fixing	NA	As Possible	20 days	Wed 25/7/2	Mon 25/7/21	Wed 25/7/2	Mon 25/7/21	Wed 25/7/2	Mon 25/7/21	0 days	1	63FS-36 days
66	Formwork Erection and Cast-in items	NA	As Possible	20 days	Thu 25/7/10	Tue 25/7/29	Thu 25/7/10	Tue 25/7/29	Thu 25/7/10	Tue 25/7/29	0 days	1	65FS-12 days
67	Concreting	NA	As Possible	4 days	Fri 25/7/18	Mon 25/7/21	Fri 25/7/18	Mon 25/7/21	Fri 25/7/18	Mon 25/7/21	0 days	0	66FS-12 days
68	**Walls**	**NA**	**As Possible**	**30 days**	**Tue 25/7/22**	**Wed 25/8/20**	**Tue 25/7/22**	**Wed 25/8/20**	**Tue 25/7/22**	**Wed 25/8/20**	**0 days**		
69	Rebar Fixing	NA	As Possible	20 days	Tue 25/7/22	Sun 25/8/10	Tue 25/7/22	Sun 25/8/10	Tue 25/7/22	Sun 25/8/10	0 days	1	67
70	Formwork Erection and Cast-in items	NA	As Possible	20 days	Fri 25/8/1	Wed 25/8/20	Fri 25/8/1	Wed 25/8/20	Fri 25/8/1	Wed 25/8/20	0 days	1	69FS-10 days
71	Concreting	NA	As Possible	4 days	Mon 25/8/11	Thu 25/8/14	Mon 25/8/11	Thu 25/8/14	Mon 25/8/11	Thu 25/8/14	0 days	0	70FS-10 days
72	Backfilling and Compaction	NA	As Possible	20 days	Fri 25/8/15	Wed 25/9/3	Fri 25/8/15	Wed 25/9/3	Fri 25/8/15	Wed 25/9/3	0 days	0	71
73	Removal of Sheetpiles	NA	As Possible	20 days	Mon 25/8/25	Sat 25/9/13	Mon 25/8/25	Sat 25/9/13	Mon 25/8/25	Sat 25/9/13	0 days	0	72FS-10 days
74	**SSNV06 CH.A100.00~CH.A200.00**	**NA**	**As Possible**	**78 days**	**Thu 25/9/4**	**Thu 25/11/20**	**Thu 25/9/4**	**Thu 25/11/20**	**Thu 25/9/4**	**Thu 25/11/20**	**0 days**		
75	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	48 days	Thu 25/9/4	Tue 25/10/21	Thu 25/9/4	Tue 25/10/21	Thu 25/9/4	Tue 25/10/21	0 days	2	73FS-10 days
76	Excavation and Lateral Support	NA	As Possible	48 days	Tue 25/9/16	Sun 25/11/2	Tue 25/9/16	Sun 25/11/2	Tue 25/9/16	Sun 25/11/2	0 days	2	75FS-36 days
77	**Ground and Edge Beams**	**NA**	**As Possible**	**28 days**	**Sun 25/9/28**	**Sat 25/10/25**	**Sun 25/9/28**	**Sat 25/10/25**	**Sun 25/9/28**	**Sat 25/10/25**	**0 days**		
78	Rebar Fixing	NA	As Possible	20 days	Sun 25/9/28	Fri 25/10/17	Sun 25/9/28	Fri 25/10/17	Sun 25/9/28	Fri 25/10/17	0 days	1	76FS-36 days
79	Formwork Erection and Cast-in items	NA	As Possible	20 days	Mon 25/10/6	Sat 25/10/25	Mon 25/10/6	Sat 25/10/25	Mon 25/10/6	Sat 25/10/25	0 days	1	78FS-12 days
80	Concreting	NA	As Possible	4 days	Tue 25/10/14	Fri 25/10/17	Tue 25/10/14	Fri 25/10/17	Tue 25/10/14	Fri 25/10/17	0 days	0	79FS-12 days
81	**Walls**	**NA**	**As Possible**	**10 days**	**Sat 25/10/18**	**Mon 25/10/27**	**Sat 25/10/18**	**Mon 25/10/27**	**Sat 25/10/18**	**###########**	**0 days**		
82	Rebar Fixing	NA	As Possible	10 days	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	0 days	1	80
83	Formwork Erection and Cast-in items	NA	As Possible	10 days	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	0 days	1	82FS-10 days
84	Concreting	NA	As Possible	4 days	Sat 25/10/18	Tue 25/10/21	Sat 25/10/18	Tue 25/10/21	Sat 25/10/18	Tue 25/10/21	0 days	0	83FS-10 days
85	Backfilling and Compaction	NA	As Possible	20 days	Wed 25/10/22	Mon 25/11/10	Wed 25/10/22	Mon 25/11/10	Wed 25/10/22	Mon 25/11/10	0 days	0	84
86	Removal of Sheetpiles	NA	As Possible	20 days	Sat 25/11/1	Thu 25/11/20	Sat 25/11/1	Thu 25/11/20	Sat 25/11/1	Thu 25/11/20	0 days	0	85FS-10 days
87	Animal Escape Ramp	Fri 26/12/4	Later Than	14 days	Fri 25/11/21	Thu 25/12/4	Fri 25/11/21	Thu 25/12/4	Sat 26/11/21	Fri 26/12/4	365 days	0	86
88	Relocate/Divert ex. Utilities	NA	As Possible	14 days	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	0 days	0	86FS-10 days
89	Demolish & relocate wall and porch YLL796/B/5,5A	NA	As Possible	14 days	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	0 days	0	86FS-10 days
90	Demolish & relocate booth, metal frame YLL796/B/16	NA	As Possible	14 days	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	0 days	0	86FS-10 days
91	Demolish & relocate wall YLL796/B/17	NA	As Possible	14 days	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	Tue 25/11/11	Mon 25/11/24	0 days	0	86FS-10 days
92	**SSNV07 CH.A0.00~CH.A100.00**	**NA**	**As Possible**	**118 days**	**Tue 25/11/25**	**Sun 26/3/22**	**Tue 25/11/25**	**Sun 26/3/22**	**Tue 25/11/25**	**Sun 26/3/22**	**0 days**		
93	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	48 days	Tue 25/11/25	Sun 26/1/11	Tue 25/11/25	Sun 26/1/11	Tue 25/11/25	Sun 26/1/11	0 days	2	88,89,90,91
94	Excavation and Lateral Support	NA	As Possible	48 days	Sun 25/12/7	Fri 26/1/23	Sun 25/12/7	Fri 26/1/23	Sun 25/12/7	Fri 26/1/23	0 days	2	93FS-36 days
95	Ground and Edge Beams	NA	As Possible	28 days	Fri 25/12/19	Thu 26/1/15	Fri 25/12/19	Thu 26/1/15	Fri 25/12/19	Thu 26/1/15	0 days		

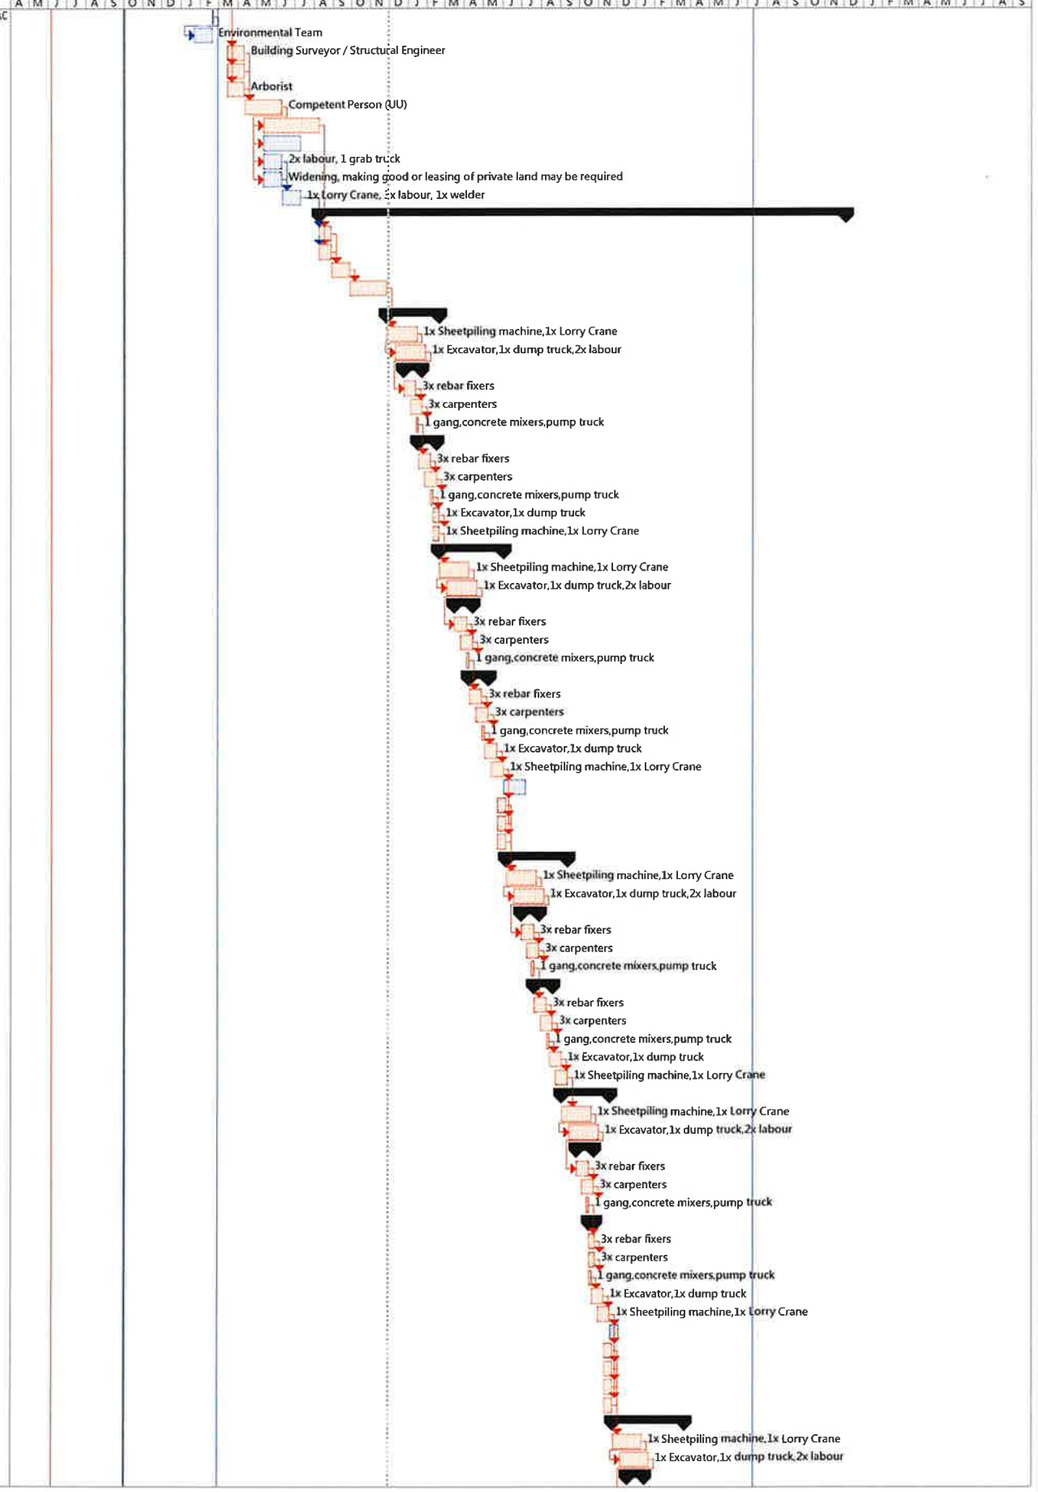


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
96	Rebar Fixing	NA	As Possible	20 days	Fri 25/12/19	Wed 26/1/7	Fri 25/12/19	Wed 26/1/7	Fri 25/12/19	Wed 26/1/7	0 days	1	94FS-36 days
97	Formwork Erection and Cast-in items	NA	As Possible	20 days	Sat 25/12/27	Thu 26/1/15	Sat 25/12/27	Thu 26/1/15	Sat 25/12/27	Thu 26/1/15	0 days	1	96FS-12 days
98	Concreting	NA	As Possible	4 days	Sun 26/1/4	Wed 26/1/7	Sun 26/1/4	Wed 26/1/7	Sun 26/1/4	Wed 26/1/7	0 days	0	97FS-12 days
99	**Walls**	NA	As Possible	50 days	Thu 26/1/8	Thu 26/2/26	Thu 26/1/8	Thu 26/2/26	Thu 26/1/8	Thu 26/2/26	0 days		
100	Rebar Fixing	NA	As Possible	20 days	Thu 26/1/8	Tue 26/1/27	Thu 26/1/8	Tue 26/1/27	Thu 26/1/8	Tue 26/1/27	0 days	1	98
101	Formwork Erection and Cast-in items	NA	As Possible	20 days	Sat 26/2/7	Thu 26/2/26	Sat 26/2/7	Thu 26/2/26	Sat 26/2/7	Thu 26/2/26	0 days	1	100FS+10 days
102	Concreting	NA	As Possible	4 days	Tue 26/2/17	Fri 26/2/20	Tue 26/2/17	Fri 26/2/20	Tue 26/2/17	Fri 26/2/20	0 days	0	101FS-10 days
103	Backfilling and Compaction	NA	As Possible	20 days	Sat 26/2/21	Thu 26/3/12	Sat 26/2/21	Thu 26/3/12	Sat 26/2/21	Thu 26/3/12	0 days	0	102
104	Removal of Sheetpiles	NA	As Possible	20 days	Tue 26/3/3	Sun 26/3/22	Tue 26/3/3	Sun 26/3/22	Tue 26/3/3	Sun 26/3/22	0 days	0	103FS-10 days
105	Pedestrian Crossing no. 2	Fri 26/12/4	No Later Than	28 days	Mon 26/3/23	Sun 26/4/19	Mon 26/3/23	Sun 26/4/19	Sat 26/11/7	Fri 26/12/4	229 days	0	104
106	Demolish & relocate metal frame YLL796/B/6	NA	As Possible	14 days	Fri 26/3/13	Thu 26/3/26	Fri 26/3/13	Thu 26/3/26	Fri 26/3/13	Thu 26/3/26	0 days	0	104FS-10 days
107	Demolish & relocate metal frame YLL796/B/7-8	NA	As Possible	14 days	Fri 26/3/13	Thu 26/3/26	Fri 26/3/13	Thu 26/3/26	Fri 26/3/13	Thu 26/3/26	0 days	0	104FS-10 days
108	**SSNV01 CH.A559.5~CH.A608.13**	NA	As Possible	121 days	Fri 26/3/27	Sat 26/7/25	Fri 26/3/27	Sat 26/7/25	Fri 26/3/27	Sat 26/7/25	0 days		
109	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	30 days	Fri 26/3/27	Sat 26/4/25	Fri 26/3/27	Sat 26/4/25	Fri 26/3/27	Sat 26/4/25	0 days	0	106,107
110	Excavation and Lateral Support	NA	As Possible	30 days	Sat 26/4/11	Sun 26/5/10	Sat 26/4/11	Sun 26/5/10	Sat 26/4/11	Sun 26/5/10	0 days	0	109FS-15 days
111	**Ground and Edge Beams**	NA	As Possible	30 days	Sun 26/4/26	Mon 26/5/25	Sun 26/4/26	Mon 26/5/25	Sun 26/4/26	Mon 26/5/25	0 days		
112	Rebar Fixing	NA	As Possible	20 days	Sun 26/4/26	Fri 26/5/15	Sun 26/4/26	Fri 26/5/15	Sun 26/4/26	Fri 26/5/15	0 days	0	110FS-15 days
113	Formwork Erection and Cast-in items	NA	As Possible	20 days	Wed 26/5/6	Mon 26/5/25	Wed 26/5/6	Mon 26/5/25	Wed 26/5/6	Mon 26/5/25	0 days	0	112FS-10 days
114	Concreting	NA	As Possible	3 days	Sat 26/5/16	Mon 26/5/18	Sat 26/5/16	Mon 26/5/18	Sat 26/5/16	Mon 26/5/18	0 days	0	113FS-10 days
115	**Walls**	NA	As Possible	30 days	Tue 26/5/19	Wed 26/6/17	Tue 26/5/19	Wed 26/6/17	Tue 26/5/19	Wed 26/6/17	0 days		
116	Rebar Fixing	NA	As Possible	20 days	Tue 26/5/19	Sun 26/6/7	Tue 26/5/19	Sun 26/6/7	Tue 26/5/19	Sun 26/6/7	0 days	0	114
117	Formwork Erection and Cast-in items	NA	As Possible	20 days	Fri 26/5/29	Wed 26/6/17	Fri 26/5/29	Wed 26/6/17	Fri 26/5/29	Wed 26/6/17	0 days	0	116FS-10 days
118	Concreting	NA	As Possible	3 days	Mon 26/6/8	Wed 26/6/10	Mon 26/6/8	Wed 26/6/10	Mon 26/6/8	Wed 26/6/10	0 days	0	117FS-10 days
119	Backfilling and Compaction	NA	As Possible	30 days	Thu 26/6/11	Fri 26/7/10	Thu 26/6/11	Fri 26/7/10	Thu 26/6/11	Fri 26/7/10	0 days	0	118
120	Removal of Sheetpiles	NA	As Possible	30 days	Fri 26/6/26	Sat 26/7/25	Fri 26/6/26	Sat 26/7/25	Fri 26/6/26	Sat 26/7/25	0 days	0	119FS-15 days
121	Pedestrian Crossing no. 1	Fri 26/12/4	No Later Than	28 days	Sun 26/7/26	Sat 26/8/22	Sun 26/7/26	Sat 26/8/22	Sat 26/11/7	Fri 26/12/4	104 days	0	120
122	**SSNV02 CH.A500.00~CH.A559.5**	NA	As Possible	119 days	Sat 26/7/11	Fri 26/11/6	Sat 26/7/11	Fri 26/11/6	Sat 26/7/11	Fri 26/11/6	0 days		
123	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	30 days	Sat 26/7/11	Sun 26/8/9	Sat 26/7/11	Sun 26/8/9	Sat 26/7/11	Sun 26/8/9	0 days	3	120FS-15 days,
124	Excavation and Lateral Support	NA	As Possible	30 days	Sun 26/7/26	Mon 26/8/24	Sun 26/7/26	Mon 26/8/24	Sun 26/7/26	Mon 26/8/24	0 days	3	123FS-15 days
125	**Ground and Edge Beams**	NA	As Possible	30 days	Mon 26/8/10	Tue 26/9/8	Mon 26/8/10	Tue 26/9/8	Mon 26/8/10	Tue 26/9/8	0 days		
126	Rebar Fixing	NA	As Possible	20 days	Mon 26/8/10	Sat 26/8/29	Mon 26/8/10	Sat 26/8/29	Mon 26/8/10	Sat 26/8/29	0 days	2	124FS-15 days
127	Formwork Erection and Cast-in items	NA	As Possible	20 days	Thu 26/8/20	Tue 26/9/8	Thu 26/8/20	Tue 26/9/8	Thu 26/8/20	Tue 26/9/8	0 days	2	126FS-10 days
128	Concreting	NA	As Possible	2 days	Sun 26/8/30	Mon 26/8/31	Sun 26/8/30	Mon 26/8/31	Sun 26/8/30	Mon 26/8/31	0 days	2	127FS-10 days
129	**Walls**	NA	As Possible	30 days	Tue 26/9/1	Wed 26/9/30	Tue 26/9/1	Wed 26/9/30	Tue 26/9/1	Wed 26/9/30	0 days		
130	Rebar Fixing	NA	As Possible	20 days	Tue 26/9/1	Sun 26/9/20	Tue 26/9/1	Sun 26/9/20	Tue 26/9/1	Sun 26/9/20	0 days	2	128
131	Formwork Erection and Cast-in items	NA	As Possible	20 days	Fri 26/9/11	Wed 26/9/30	Fri 26/9/11	Wed 26/9/30	Fri 26/9/11	Wed 26/9/30	0 days	2	130FS-10 days
132	Concreting	NA	As Possible	2 days	Mon 26/9/21	Tue 26/9/22	Mon 26/9/21	Tue 26/9/22	Mon 26/9/21	Tue 26/9/22	0 days	2	131FS-10 days
133	Backfilling and Compaction	NA	As Possible	30 days	Wed 26/9/23	Thu 26/10/22	Wed 26/9/23	Thu 26/10/22	Wed 26/9/23	Thu 26/10/22	0 days	0	132
134	Removal of Sheetpiles	NA	As Possible	30 days	Thu 26/10/8	Fri 26/11/6	Thu 26/10/8	Fri 26/11/6	Thu 26/10/8	Fri 26/11/6	0 days	0	133FS-15 days
135	Modify ex. Channel at Outlet	Fri 26/12/4	No Later Than	21 days	Sat 26/11/7	Fri 26/11/27	Sat 26/11/7	Fri 26/11/27	Sat 26/11/14	Fri 26/12/4	7 days	0	134
136	Connection to ex. Stream	Fri 26/12/4	No Later Than	28 days	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	0 days	0	134
137	U-channels	Fri 26/12/4	No Later Than	28 days	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	0 days	0	134
138	Facing stone	Fri 26/12/4	No Later Than	28 days	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	0 days	0	134
139	ABWF works	Fri 26/12/4	No Later Than	28 days	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	0 days	0	134
140	Bedding works	Fri 26/12/4	No Later Than	28 days	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	Sat 26/11/7	Fri 26/12/4	0 days	0	134
106													
107	**Section II**	NA	As Possible	1071 days	Tue 23/5/30	Mon 26/5/4	Tue 23/5/30	Mon 26/5/4	Tue 23/5/30	Mon 26/5/4	0 days		
2	access date of Portion B	########	No Later Than	210 days	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	0 days	0	\\WingTatNasC
3	section II (Tai Wo)	Mon 26/5/4	No Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days	0	\\WingTatNasC
4	Planned Completion Day	Mon 26/5/4	No Later Than	251 days	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	Wed 25/8/27	Mon 26/5/4	0 days		3
5	Early access [A]	NA	As Possible	144 days	Tue 23/5/30	Fri 23/10/20	Tue 23/5/30	Fri 23/10/20	Tue 23/5/30	Fri 23/10/20	0 days	0	\\WingTatNasC
6	**Site Establishment**	NA	As Possible	461 days	Tue 23/9/26	Sun 24/12/29	Tue 23/9/26	Sun 24/12/29	Sat 23/10/21	Mon 26/5/4	25 days		
7	Prepare and Accept Temp. Works Design and Method Statement	Mon 26/5/4	No Later Than	461 days	Tue 23/9/26	Sun 24/12/29	Tue 23/9/26	Sun 24/12/29	Wed 25/1/29	Mon 26/5/4	491 days	0	\\WingTatNasC
8	Public Liaison and Negotiation with Village Rep.	NA	As Possible	103 days	Fri 23/10/20	Tue 24/1/30	Fri 23/10/20	Tue 24/1/30	Wed 23/12/20	Sun 24/3/31	61 days	0	5FS-1 day
9	Initial Survey	NA	As Possible	80 days	Sat 23/10/21	Mon 24/1/8	Sat 23/10/21	Mon 24/1/8	Sat 23/10/21	Mon 24/1/8	0 days	0	5
10	Initial Safety & Environmental measures	NA	As Possible	80 days	Sat 23/10/21	Mon 24/1/8	Sat 23/10/21	Mon 24/1/8	Sat 23/10/21	Mon 24/1/8	0 days	0	5
12	EIAO Commencement of Construction	NA	As Possible	1 day	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Mon 24/4/8	Mon 24/4/8	47 days	0	\\WingTatNasC
13	Environmental Baseline Monitoring	NA	As Possible	15 days	Tue 24/1/23	Tue 24/2/6	Tue 24/1/23	Tue 24/2/6	Sun 24/3/10	Sun 24/3/24	47 days	0	12FS-30 days
14	**Subcontracting of works**	NA	As Possible	120 days	Sat 23/10/21	Sat 24/2/17	Sat 23/10/21	Sat 24/2/17	Wed 24/6/26	Wed 24/10/23	249 days		
15	Preparation of tendering documents	NA	As Possible	30 days	Sat 23/10/21	Sun 23/11/19	Sat 23/10/21	Sun 23/11/19	Wed 24/6/26	Thu 24/7/25	249 days	0	5
16	EWN007 Ambiguities on drawings	NA	As Possible	60 days	Mon 23/11/20	Thu 24/1/18	Mon 23/11/20	Thu 24/1/18	Fri 24/7/26	Mon 24/9/23	249 days	0	15
17	C9 Tendering procedure for Tai Wo RC works	NA	As Possible	30 days	Fri 24/1/19	Sat 24/2/17	Fri 24/1/19	Sat 24/2/17	Tue 24/9/24	Wed 24/10/23	249 days	0	16
19	Setup of instrumentation and monitoring	NA	As Possible	76 days	Tue 24/1/9	Sun 24/3/24	Tue 24/1/9	Sun 24/3/24	Tue 24/1/9	Sun 24/3/24	0 days	0	10,9
20	Condition Survey [A]	NA	As Possible	15 days	Tue 24/1/9	Tue 24/1/23	Tue 24/1/9	Tue 24/1/23	Sun 24/3/10	Sun 24/3/24	61 days	0	10,9
21	Tree Survey [A]	NA	As Possible	15 days	Tue 24/1/9	Tue 24/1/23	Tue 24/1/9	Tue 24/1/23	Wed 24/1/17	Wed 24/1/31	8 days	0	10,9
22	[PMIxxx] TPRP for Additional Trees (impact to be ascertained)	NA	As Possible	60 days	Wed 24/1/24	Sat 24/3/23	Wed 24/1/24	Sat 24/3/23	Thu 24/2/1	Sun 24/3/31	8 days	0	21
23	Establish access(es) to channels	NA	As Possible	15 days	Tue 24/1/9	Tue 24/1/23	Tue 24/1/9	Tue 24/1/23	Tue 24/1/9	Tue 24/1/23	0 days	0	10,9
24	[NCExxx] [EWN008] Blockade of access by others (impact to be ascertained)	NA	As Possible	68 days	Wed 24/1/24	Sun 24/3/31	Wed 24/1/24	Sun 24/3/31	Wed 24/1/24	Sun 24/3/31	0 days	0	23
25	UU detection [A]	NA	As Possible	7 days	Wed 24/1/24	Tue 24/1/30	Wed 24/1/24	Tue 24/1/30	Mon 24/3/25	Sun 24/3/31	61 days	0	20,23
26	Site Clearance [A]	NA	As Possible	7 days	Mon 24/3/25	Sun 24/3/31	Mon 24/3/25	Sun 24/3/31	Mon 24/3/25	Sun 24/3/31	0 days	0	21,19,13
27	**Drainage Channels Works (Dry Season Oct-Mar only)**	NA	As Possible	764 days	Mon 24/4/1	Mon 26/5/4	Mon 24/4/1	Mon 26/5/4	Mon 24/4/1	Mon 26/5/4	0 days		
28	[NCExxx] No works for wet season	NA	As Possible	183 days	Mon 24/4/1	Mon 24/9/30	Mon 24/4/1	Mon 24/9/30	Mon 24/4/1	Mon 24/9/30	0 days		26,25,8,24,22
29	Guarding / Barrier / Hoarding	NA	As Possible	22 days	Tue 24/10/1	Tue 24/10/22	Tue 24/10/1	Tue 24/10/22	Tue 24/10/1	Tue 24/10/22	0 days	0	28
30	Demolish fences and temp. structure	NA	As Possible	14 days	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	0 days	0	28
31	Demolish & relocate hoarding, fencing YLL803	NA	As Possible	14 days	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	0 days	0	28
32	**CH.A200~CH.A288.29**	NA	As Possible	118 days	Tue 24/10/15	Sun 25/2/9	Tue 24/10/15	Sun 25/2/9	Tue 24/10/15	Sun 25/2/9	0 days		
33	Sheetpiling & Temp. Drainage Diversion (for non-open-cut portions)	NA	As Possible	45 days	Tue 24/10/15	Thu 24/11/28	Tue 24/10/15	Thu 24/11/28	Tue 24/10/15	Thu 24/11/28	0 days	1	30,31,29FS-8 d
34	Excavation and Lateral Support	NA	As Possible	45 days	Thu 24/10/24	Sat 24/12/7	Thu 24/10/24	Sat 24/12/7	Thu 24/10/24	Sat 24/12/7	0 days	1	33FS-36 days,1
35	**Base Slab**	NA	As Possible	49 days	Sat 24/11/2	Fri 24/12/20	Sat 24/11/2	Fri 24/12/20	Sat 24/11/2	Fri 24/12/20	0 days		
36	Rebar Fixing	NA	As Possible	35 days	Sat 24/11/2	Fri 24/12/6	Sat 24/11/2	Fri 24/12/6	Sat 24/11/2	Fri 24/12/6	0 days	1	34FS-36 days
37	Formwork Erection and Cast-in items	NA	As Possible	35 days	Sat 24/11/16	Fri 24/12/20	Sat 24/11/16	Fri 24/12/20	Sat 24/11/16	Fri 24/12/20	0 days	1	36FS-21 days
38	Concreting	NA	As Possible	1 day	Sat 24/11/30	Sat 24/11/30	Sat 24/11/30	Sat 24/11/30	Sat 24/11/30	Sat 24/11/30	0 days	0	37FS-21 days

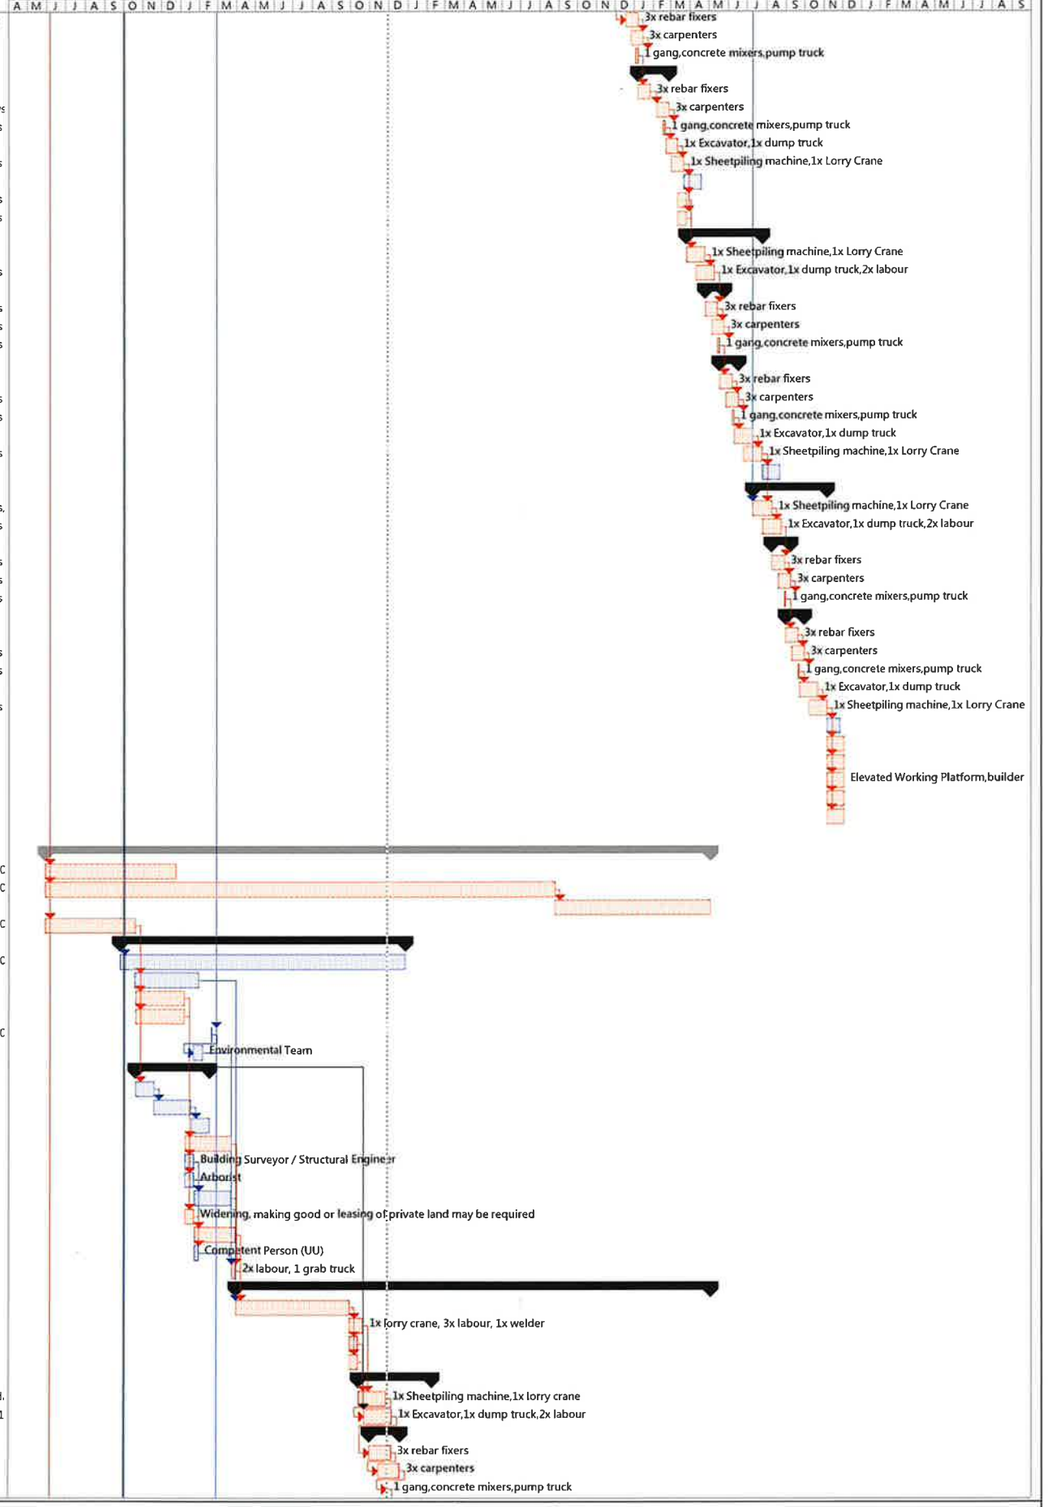


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
39	**Walls**	NA	As Possible	49 days	Sun 24/12/1	Sat 25/1/18	Sun 24/12/1	Sat 25/1/18	Sun 24/12/1	Sat 25/1/18	0 days	0	
40	Rebar Fixing	NA	As Possible	35 days	Sun 24/12/1	Sat 25/1/4	Sun 24/12/1	Sat 25/1/4	Sun 24/12/1	Sat 25/1/4	0 days	1	38
41	Formwork Erection and Cast-in items	NA	As Possible	35 days	Sun 24/12/15	Sat 25/1/18	Sun 24/12/15	Sat 25/1/18	Sun 24/12/15	Sat 25/1/18	0 days	1	40FS-21 days
42	Concreting	NA	As Possible	1 day	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	0 days	0	41FS-21 days
43	Backfilling and Compaction	NA	As Possible	30 days	Mon 24/12/30	Tue 25/1/28	Mon 24/12/30	Tue 25/1/28	Mon 24/12/30	Tue 25/1/28	0 days	0	42
44	Removal of Sheetpiles	NA	As Possible	30 days	Sat 25/1/11	Sun 25/2/9	Sat 25/1/11	Sun 25/2/9	Sat 25/1/11	Sun 25/2/9	0 days	0	43FS-18 days
45	Connection to ex. Channel at Outlet	Mon 26/5/4	Later Than	16 days	Thu 25/1/23	Fri 25/2/7	Thu 25/1/23	Fri 25/2/7	Thu 25/1/23	Fri 25/2/7	0 days	0	44FS-18 days
46	**CH.A100~CH.A200**	NA	**As Possible**	**67 days**	**Fri 25/1/24**	**Mon 25/3/31**	**Fri 25/1/24**	**Mon 25/3/31**	**Fri 25/1/24**	**Mon 25/3/31**	**0 days**		
47	Sheetpiling & Temp. Drainage Diversion (for non-open-cut portions)	NA	As Possible	45 days	Fri 25/1/24	Sun 25/3/9	Fri 25/1/24	Sun 25/3/9	Fri 25/1/24	Sun 25/3/9	0 days	1	45FS-15 days
48	Excavation and Lateral Support	NA	As Possible	45 days	Sun 25/2/2	Tue 25/3/18	Sun 25/2/2	Tue 25/3/18	Sun 25/2/2	Tue 25/3/18	0 days	1	47FS-36 days
49	**Base Slab**	NA	**As Possible**	49 days	**Tue 25/2/11**	**Mon 25/3/31**	**Tue 25/2/11**	**Mon 25/3/31**	**Tue 25/2/11**	**Mon 25/3/31**	**0 days**		
50	Rebar Fixing	NA	As Possible	35 days	Tue 25/2/11	Mon 25/3/17	Tue 25/2/11	Mon 25/3/17	Tue 25/2/11	Mon 25/3/17	0 days	1	48FS-36 days
51	Formwork Erection and Cast-in items	NA	As Possible	35 days	Tue 25/2/25	Mon 25/3/31	Tue 25/2/25	Mon 25/3/31	Tue 25/2/25	Mon 25/3/31	0 days	1	50FS-21 days
52	Concreting	NA	As Possible	1 day	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	0 days	0	51FS-1 day
53	No works at wet season	NA	As Possible	183 days	Tue 25/4/1	Tue 25/9/30	Tue 25/4/1	Tue 25/9/30	Tue 25/4/1	Tue 25/9/30	0 days	0	52
54	**CH.A100~CH.A200 (continue)**	NA	**As Possible**	78 days	**Wed 25/10/1**	**Wed 25/12/17**	**Wed 25/10/1**	**Wed 25/12/17**	**Wed 25/10/1**	**Wed 25/12/17**	**0 days**		
55	**Walls**	NA	**As Possible**	49 days	**Wed 25/10/1**	**Tue 25/11/18**	**Wed 25/10/1**	**Tue 25/11/18**	**Wed 25/10/1**	**Tue 25/11/18**	**0 days**		
56	Rebar Fixing	NA	As Possible	35 days	Wed 25/10/1	Tue 25/11/4	Wed 25/10/1	Tue 25/11/4	Wed 25/10/1	Tue 25/11/4	0 days	1	53
57	Formwork Erection and Cast-in items	NA	As Possible	35 days	Wed 25/10/15	Tue 25/11/18	Wed 25/10/15	Tue 25/11/18	Wed 25/10/15	Tue 25/11/18	0 days	1	56FS-21 days
58	Concreting	NA	As Possible	1 day	Wed 25/10/29	Wed 25/10/29	Wed 25/10/29	Wed 25/10/29	Wed 25/10/29	Wed 25/10/29	0 days	0	57FS-21 days
59	Backfilling and Compaction	NA	As Possible	35 days	Thu 25/10/30	Wed 25/12/3	Thu 25/10/30	Wed 25/12/3	Thu 25/10/30	Wed 25/12/3	0 days	0	58
60	Removal of Sheetpiles	NA	As Possible	35 days	Thu 25/11/13	Wed 25/12/17	Thu 25/11/13	Wed 25/12/17	Thu 25/11/13	Wed 25/12/17	0 days	0	59FS-21 days
61	**CH.A19.69~CH.A100**	NA	**As Possible**	**125 days**	**Thu 25/11/27**	**Tue 26/3/31**	**Thu 25/11/27**	**Tue 26/3/31**	**Thu 25/11/27**	**Tue 26/3/31**	**0 days**		
62	Sheetpiling & Temp. Drainage Diversion (for non-open-cut portions)	NA	As Possible	45 days	Thu 25/11/27	Sat 26/1/10	Thu 25/11/27	Sat 26/1/10	Thu 25/11/27	Sat 26/1/10	0 days	1	60FS-21 days
63	Excavation and Lateral Support	NA	As Possible	45 days	Sat 25/12/6	Mon 26/1/19	Sat 25/12/6	Mon 26/1/19	Sat 25/12/6	Mon 26/1/19	0 days	1	62FS-36 days
64	**Base Slab**	NA	**As Possible**	49 days	**Mon 25/12/15**	**Sun 26/2/1**	##########	**Sun 26/2/1**	##########	**Sun 26/2/1**	**0 days**		
65	Rebar Fixing	NA	As Possible	35 days	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	0 days	1	63FS-36 days
66	Formwork Erection and Cast-in items	NA	As Possible	35 days	Mon 25/12/29	Sun 26/2/1	Mon 25/12/29	Sun 26/2/1	Mon 25/12/29	Sun 26/2/1	0 days	1	65FS-21 days
67	Concreting	NA	As Possible	1 day	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	0 days	0	66FS-21 days
68	**Walls**	NA	**As Possible**	49 days	**Tue 26/1/13**	**Mon 26/3/2**	**Tue 26/1/13**	**Mon 26/3/2**	**Tue 26/1/13**	**Mon 26/3/2**	**0 days**		
69	Rebar Fixing	NA	As Possible	35 days	Tue 26/1/13	Mon 26/2/16	Tue 26/1/13	Mon 26/2/16	Tue 26/1/13	Mon 26/2/16	0 days	1	67
70	Formwork Erection and Cast-in items	NA	As Possible	35 days	Tue 26/1/27	Mon 26/3/2	Tue 26/1/27	Mon 26/3/2	Tue 26/1/27	Mon 26/3/2	0 days	1	69FS-21 days
71	Concreting	NA	As Possible	1 day	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	0 days	0	70FS-21 days
72	Backfilling and Compaction	NA	As Possible	35 days	Wed 26/2/11	Tue 26/3/17	Wed 26/2/11	Tue 26/3/17	Wed 26/2/11	Tue 26/3/17	0 days	0	71
73	Removal of Sheetpiles	NA	As Possible	35 days	Wed 26/2/25	Tue 26/3/31	Wed 26/2/25	Tue 26/3/31	Wed 26/2/25	Tue 26/3/31	0 days	0	72FS-21 days
74	900 pipe with flap valve	Mon 26/5/4	Later Than	21 days	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	0 days	0	73FS-21 days
75	Box Culvert & Pedestrian Crossing	Mon 26/5/4	Later Than	21 days	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	0 days	0	73FS-21 days
76	ABWF works	Mon 26/5/4	Later Than	21 days	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	0 days	0	73FS-21 days
77	Bedding works	Mon 26/5/4	Later Than	21 days	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	Wed 26/3/11	Tue 26/3/31	0 days	0	73FS-21 days
78	No works at wet season	Mon 26/5/4	Later Than	34 days	Wed 26/4/1	Mon 26/5/4	Wed 26/4/1	Mon 26/5/4	Wed 26/4/1	Mon 26/5/4	0 days	0	74,75,76,77
79	**U-Channel Works**	NA	**As Possible**	41 days	**Sat 26/3/14**	**Thu 26/4/23**	**Sat 26/3/14**	**Thu 26/4/23**	**Sat 26/3/14**	**Thu 26/4/23**	**0 days**		
80	**CH.A0.00~CH.A16.40,900CU,L=16.40**	NA	**As Possible**	41 days	**Sat 26/3/14**	**Thu 26/4/23**	**Sat 26/3/14**	**Thu 26/4/23**	**Sat 26/3/14**	**Thu 26/4/23**	**0 days**		
81	Excavation and Lateral Support	NA	As Possible	30 days	Sat 26/3/14	Sun 26/4/12	Sat 26/3/14	Sun 26/4/12	Sat 26/3/14	Sun 26/4/12	0 days	1	72FS-4 days
82	Channel Formwork Erection	NA	As Possible	30 days	Wed 26/3/25	Thu 26/4/23	Wed 26/3/25	Thu 26/4/23	Wed 26/3/25	Thu 26/4/23	0 days	1	81FS-19 days
83	Concreting	NA	As Possible	1 day	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	0 days	0	82FS-20 days
84	**Drain Laying Works**	NA	**As Possible**	30 days	**Sun 26/4/5**	**Mon 26/5/4**	**Sun 26/4/5**	**Mon 26/5/4**	**Sun 26/4/5**	**Mon 26/5/4**	**0 days**		
85	**CH.A16.40~CH.A19.69,900PC,B,L=3.30,D=1.5**	NA	**As Possible**	30 days	**Sun 26/4/5**	**Mon 26/5/4**	**Sun 26/4/5**	**Mon 26/5/4**	**Sun 26/4/5**	**Mon 26/5/4**	**0 days**		
86	Excavation and Lateral Support	NA	As Possible	18 days	Sun 26/4/5	Wed 26/4/22	Sun 26/4/5	Wed 26/4/22	Sun 26/4/5	Wed 26/4/22	0 days	0	83
87	Drain Laying	NA	As Possible	14 days	Mon 26/4/13	Sun 26/4/26	Mon 26/4/13	Sun 26/4/26	Mon 26/4/13	Sun 26/4/26	0 days	0	86FS-10 days
88	Bedding and Backfilling	NA	As Possible	9 days	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	0 days	0	87FS-5 days
89	Reinstatement	Mon 26/5/4	Later Than	9 days	Sun 26/4/26	Mon 26/5/4	Sun 26/4/26	Mon 26/5/4	Sun 26/4/26	Mon 26/5/4	0 days	0	88FS-5 days
108													
109	**Section III**	NA	**As Possible**	**1225 days**	**Tue 23/5/30**	**Mon 26/10/5**	**Tue 23/5/30**	**Mon 26/10/5**	**Tue 23/5/30**	**Fri 27/4/2**	**0 days**		
2	access date of Portion C1 & C2	Fri 24/2/23	Later Than	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	0 days	0	\\WingTatNasC
3	section III (Lin Fa Tei)	#########	Later Than	1155 days	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	Tue 23/5/30	Mon 26/7/27	0 days	0	\\WingTatNasC
4	Planned Completion Day	#########	Later Than	70 days	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	Tue 26/7/28	Mon 26/10/5	0 days	0	3
5	Early access (partial) [A]	NA	As Possible	200 days	Tue 23/5/30	Fri 23/12/15	Tue 23/5/30	Fri 23/12/15	Wed 23/8/23	Sat 24/3/9	85 days	0	\\WingTatNasC
6	**Site Establishment**	NA	**As Possible**	**989 days**	**Tue 23/9/12**	**Wed 26/5/27**	**Tue 23/9/12**	**Wed 26/5/27**	**Wed 23/9/27**	**Fri 27/4/2**	**15 days**		
7	Prepare and Accept Temp. Works Design and Method Statement	NA	As Possible	975 days	Tue 23/9/26	Wed 26/5/27	Tue 23/9/26	Wed 26/5/27	Tue 23/10/31	Wed 26/7/1	35 days	0	\\WingTatNasC
8	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	164 days	Tue 23/9/12	Thu 24/2/22	Tue 23/9/12	Thu 24/2/22	Wed 23/9/27	Fri 24/3/8	15 days	0	\\WingTatNasC
9	Initial Survey	NA	As Possible	825 days	Fri 24/2/23	Wed 26/5/27	Fri 24/2/23	Wed 26/5/27	Fri 24/3/29	Wed 26/7/1	35 days	0	8,5FS-1 day
11	Initial Safety & Environmental measures [A]	NA	As Possible	14 days	Fri 24/2/23	Thu 24/3/7	Fri 24/2/23	Thu 24/3/7	Sat 24/3/9	Fri 24/3/22	15 days	0	8,5FS-1 day
13	EIAO Commencement of Construction [A]	NA	As Possible	28 days	Wed 24/2/21	Tue 24/3/19	Wed 24/2/21	Tue 24/3/19	Tue 26/9/8	Mon 26/10/5	930 days	0	\\WingTatNasC
15	Environmental Baseline Monitoring [A]	NA	As Possible	15 days	Mon 24/2/19	Mon 24/3/4	Mon 24/2/19	Mon 24/3/4	Fri 27/3/19	Fri 27/4/2	1124 days	0	13FS-30 days
16	Subcontracting of works	#########	Later Than	250 days	Sat 23/12/16	Wed 24/8/21	Sat 23/12/16	Wed 24/8/21	Thu 26/1/29	Mon 26/10/5	775 days	0	5
17	Setup of instrumentation and monitoring [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	Fri 24/3/8	Fri 24/3/22	Sat 24/3/23	Sat 24/4/6	15 days	0	11
18	Condition Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	Fri 24/3/8	Fri 24/3/22	Sat 24/3/23	Sat 24/4/6	15 days	0	11
19	Freshwater Crab Translocation Plan [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	Fri 24/3/8	Fri 24/3/22	Sat 24/3/23	Sat 24/4/6	15 days	0	11
20	Archaeological Survey	NA	As Possible	300 days	Fri 24/3/8	Wed 25/1/1	Fri 24/3/8	Wed 25/1/1	Fri 25/7/4	Wed 26/4/29	483 days	0	11
21	Tree Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	Fri 24/3/8	Fri 24/3/22	Sat 24/3/23	Sat 24/4/6	15 days	0	11
22	Vegetation Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	Fri 24/3/8	Fri 24/3/22	Sat 24/3/23	Sat 24/4/6	15 days	0	11
23	UU detection [A]	NA	As Possible	15 days	Sat 24/3/23	Sat 24/4/6	Sat 24/3/23	Sat 24/4/6	Sun 24/4/7	Sun 24/4/21	15 days	0	18,19
24	Site Clearance [A]	NA	As Possible	15 days	Sat 24/3/23	Sat 24/4/6	Sat 24/3/23	Sat 24/4/6	Sun 24/4/7	Sun 24/4/21	15 days	0	21,17,11,22
25	Establish access(es) to channels [A]	#########	Later Than	25 days	Sun 24/4/7	Wed 24/5/1	Sun 24/4/7	Wed 24/5/1	Mon 24/4/22	Thu 24/5/16	15 days	0	24,23
26	Guarding / Barrier / Hoarding [A]	NA	As Possible	25 days	Sun 24/4/7	Wed 24/5/1	Sun 24/4/7	Wed 24/5/1	Mon 24/4/22	Thu 24/5/16	15 days	0	24,23
27	**Drainage Channels Works**	NA	**As Possible**	**872 days**	**Thu 24/5/2**	**Sun 26/9/20**	**Thu 24/5/2**	**Sun 26/9/20**	**Fri 24/5/17**	**Fri 27/4/2**	**15 days**		
28	Demolish & relocate retaining wall YLL795/A/4-5 [A]	NA	As Possible	30 days	Thu 24/5/2	Fri 24/5/31	Thu 24/5/2	Fri 24/5/31	Fri 24/5/17	Sat 24/6/15	15 days	0	26,25
29	Pedestrian & Vehicular Crossing no. 1 [A]	NA	As Possible	45 days	Sat 24/5/11	Mon 24/6/24	Sat 24/5/11	Mon 24/6/24	Sun 24/5/26	Tue 24/7/9	15 days	4	28FS-21 days
30	CLP Cable Trough	NA	As Possible	30 days	Tue 24/6/25	Wed 24/7/24	Tue 24/6/25	Wed 24/7/24	Thu 27/3/4	Fri 27/4/2	982 days	3	29
31	**LFT06 CH.A173.5~CH.A227.75 (PVC1)**	NA	**As Possible**	**123 days**	**Tue 24/6/18**	**Fri 24/10/18**	**Tue 24/6/18**	**Fri 24/10/18**	**Wed 24/7/3**	**Sat 24/11/2**	**15 days**		
32	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	40 days	Tue 24/6/18	Sat 24/7/27	Tue 24/6/18	Sat 24/7/27	Wed 24/7/3	Sun 24/8/11	15 days	1	29FS-7 days
33	Excavation and Lateral Support [A]	NA	As Possible	40 days	Sat 24/7/13	Wed 24/8/21	Sat 24/7/13	Wed 24/8/21	Sun 24/7/28	Thu 24/9/5	15 days	1	32FS-15 days

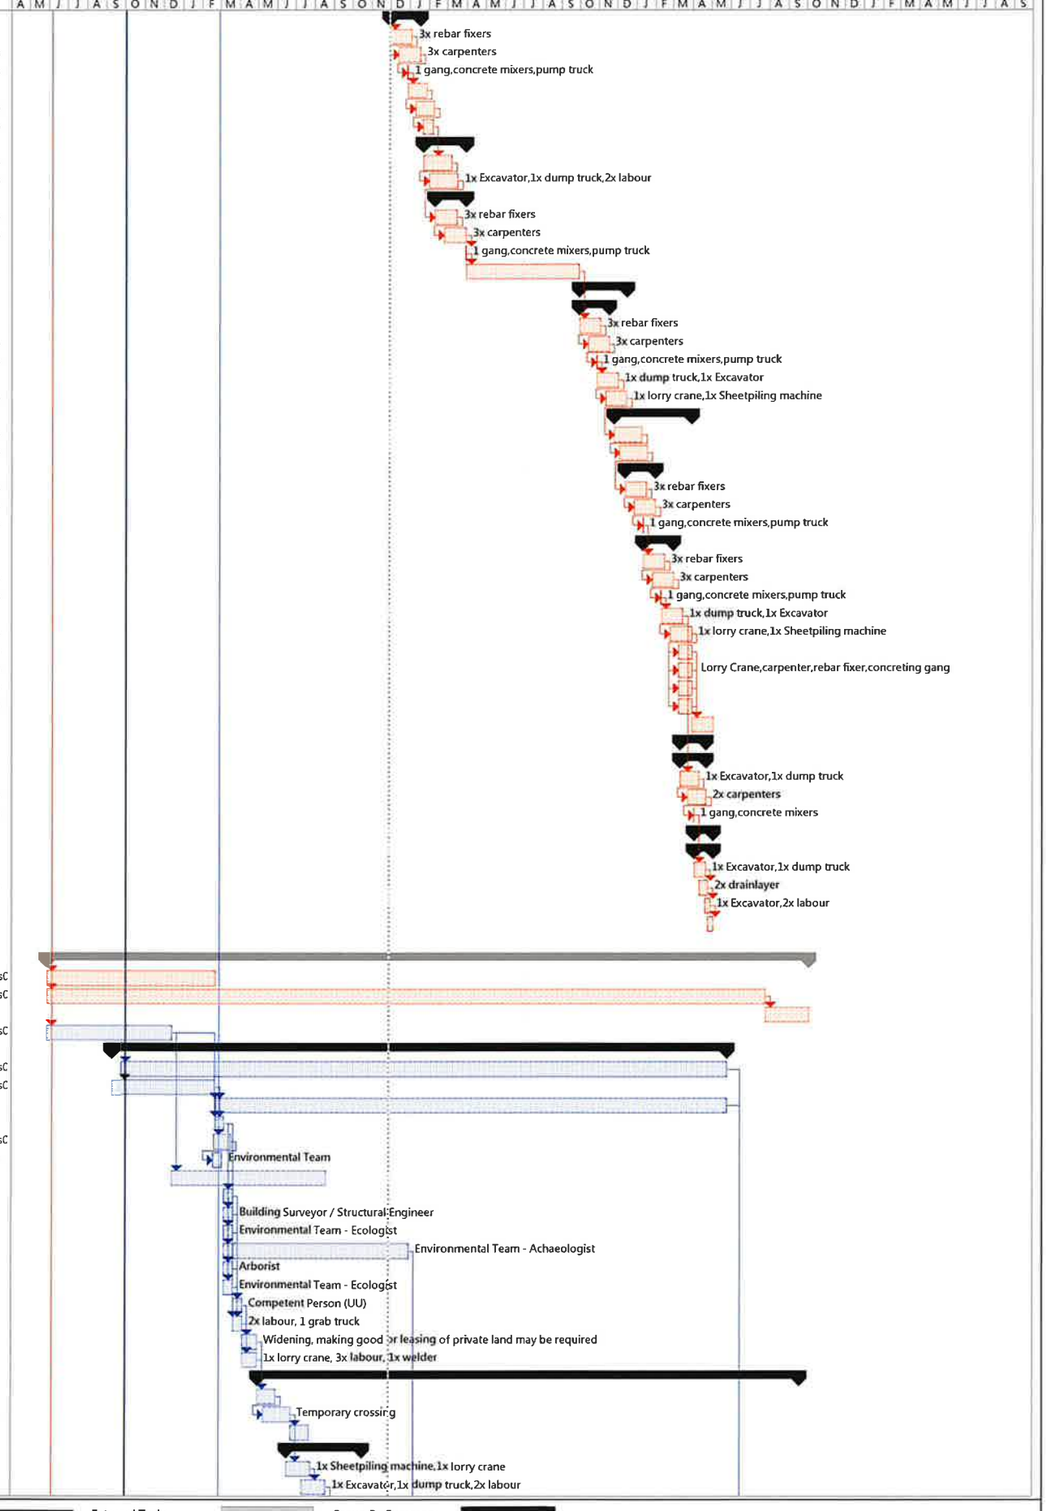


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
34	**Ground and Edge Beams**	NA	As Possible	**41 days**	Mon 24/8/5	Sat 24/9/14	Mon 24/8/5	Sat 24/9/14	Tue 24/8/20	Sun 24/9/29	**15 days**		
35	Install precast reinforcement cage (ground beam) [A]	NA	As Possible	28 days	Mon 24/8/5	Sun 24/9/1	Mon 24/8/5	Sun 24/9/1	Tue 24/8/20	Mon 24/9/16	15 days	0	33FS-17 days
36	Rebar Fixing [A]	NA	As Possible	25 days	Tue 24/8/13	Fri 24/9/6	Tue 24/8/13	Fri 24/9/6	Wed 24/8/28	Sat 24/9/21	15 days	1	35FS-20 days
37	Formwork Erection and Cast-in items [A]	NA	As Possible	25 days	Wed 24/8/21	Sat 24/9/14	Wed 24/8/21	Sat 24/9/14	Thu 24/9/5	Sun 24/9/29	15 days	1	36FS-17 days
38	Concreting [A]	NA	As Possible	1 day	Thu 24/8/29	Thu 24/8/29	Thu 24/8/29	Thu 24/8/29	Fri 24/9/13	Fri 24/9/13	15 days	0	37FS-17 days
39	**Walls**	NA	As Possible	**33 days**	Fri 24/8/30	**Tue 24/10/1**	Fri 24/8/30	**Tue 24/10/1**	**Sat 24/9/14**	**Wed 24/10/16**	**15 days**		
40	Rebar Fixing	NA	As Possible	25 days	Fri 24/8/30	Mon 24/9/23	Fri 24/8/30	Mon 24/9/23	Sat 24/9/14	Tue 24/10/8	15 days	1	38
41	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sat 24/9/7	Tue 24/10/1	Sat 24/9/7	Tue 24/10/1	Sun 24/9/22	Wed 24/10/16	15 days	1	40FS-17 days
42	Concreting	NA	As Possible	1 day	Sun 24/9/15	Sun 24/9/15	Sun 24/9/15	Sun 24/9/15	Mon 24/9/30	Mon 24/9/30	15 days	0	41FS-17 days
43	Backfilling and Compaction	NA	As Possible	25 days	Mon 24/9/16	Thu 24/10/10	Mon 24/9/16	Thu 24/10/10	Tue 24/10/1	Fri 24/10/25	15 days	0	42
44	Removal of Sheetpiles	NA	As Possible	25 days	Tue 24/9/24	Fri 24/10/18	Tue 24/9/24	Fri 24/10/18	Wed 24/10/9	Sat 24/11/2	15 days	0	43FS-17 days
45	**LFT07 CH.A227.5~CH.A300.75**	NA	As Possible	**109 days**	**Mon 24/9/9**	**Thu 24/12/26**	**Mon 24/9/9**	**Thu 24/12/26**	**Tue 24/9/24**	**Fri 25/1/10**	**15 days**		
46	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	33 days	Mon 24/9/9	Fri 24/10/11	Mon 24/9/9	Fri 24/10/11	Tue 24/9/24	Sat 24/10/26	15 days	0	44FS-40 days
47	Excavation and Lateral Support [A]	NA	As Possible	33 days	Fri 24/9/27	Tue 24/10/29	Fri 24/9/27	Tue 24/10/29	Sat 24/10/12	Wed 24/11/13	15 days	0	46FS-15 days
48	**Ground and Edge Beams**	NA	As Possible	**41 days**	**Sun 24/10/13**	**Fri 24/11/22**	**Sun 24/10/13**	**Fri 24/11/22**	##########	**Sat 24/12/7**	**15 days**		
49	Install precast reinforcement cage (ground beam) [A]	NA	As Possible	28 days	Sun 24/10/13	Sat 24/11/9	Sun 24/10/13	Sat 24/11/9	Mon 24/10/28	Sun 24/11/24	15 days	0	47FS-17 days
50	Rebar Fixing [A]	NA	As Possible	25 days	Mon 24/10/21	Thu 24/11/14	Mon 24/10/21	Thu 24/11/14	Tue 24/11/5	Fri 24/11/29	15 days	0	49FS-20 days
51	Formwork Erection and Cast-in items [A]	NA	As Possible	25 days	Tue 24/10/29	Fri 24/11/22	Tue 24/10/29	Fri 24/11/22	Wed 24/11/13	Sat 24/12/7	15 days	0	50FS-17 days
52	Concreting [A]	NA	As Possible	1 day	Wed 24/11/6	Wed 24/11/6	Wed 24/11/6	Wed 24/11/6	Thu 24/11/21	Thu 24/11/21	15 days	0	51FS-17 days
53	**Walls**	NA	As Possible	**33 days**	**Thu 24/11/7**	**Mon 24/12/9**	**Thu 24/11/7**	**Mon 24/12/9**	**Fri 24/11/22**	**Tue 24/12/24**	**15 days**		
54	Rebar Fixing	NA	As Possible	25 days	Thu 24/11/7	Sun 24/12/1	Thu 24/11/7	Sun 24/12/1	Fri 24/11/22	Mon 24/12/16	15 days	0	52
55	Formwork Erection and Cast-in items	NA	As Possible	25 days	Fri 24/11/15	Mon 24/12/9	Fri 24/11/15	Mon 24/12/9	Sat 24/11/30	Tue 24/12/24	15 days	0	54FS-17 days
56	Concreting	NA	As Possible	1 day	Sat 24/11/23	Sat 24/11/23	Sat 24/11/23	Sat 24/11/23	Sun 24/12/8	Sun 24/12/8	15 days	0	55FS-17 days
57	Backfilling and Compaction	NA	As Possible	25 days	Sun 24/11/24	Wed 24/12/18	Sun 24/11/24	Wed 24/12/18	Mon 24/12/9	Thu 25/1/2	15 days	0	56
58	Removal of Sheetpiles	NA	As Possible	25 days	Mon 24/12/2	Thu 24/12/26	Mon 24/12/2	Thu 24/12/26	Tue 24/12/17	Fri 25/1/10	15 days	0	57FS-17 days
59	Pedestrian & Vehicular Crossing no. 2	########	Later Than	28 days	Tue 24/12/10	Mon 25/1/6	Tue 24/12/10	Mon 25/1/6	Tue 26/9/8	Mon 26/10/5	637 days	4	58FS-17 days
60	**LFT05 CH.A163.00~CH.A173.50**	NA	As Possible	**72 days**	**Tue 24/12/10**	**Wed 25/2/19**	**Tue 24/12/10**	**Wed 25/2/19**	**Wed 24/12/25**	**Thu 25/3/6**	**15 days**		
61	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	27 days	Tue 24/12/10	Sun 25/1/5	Tue 24/12/10	Sun 25/1/5	Wed 24/12/25	Mon 25/1/20	15 days	0	58FS-17 days
62	Excavation and Lateral Support	NA	As Possible	27 days	Sun 24/12/22	Fri 25/1/17	Sun 24/12/22	Fri 25/1/17	Mon 25/1/6	Sat 25/2/1	15 days	0	61FS-15 days
63	**Ground and Edge Beams**	NA	As Possible	**33 days**	**Wed 25/1/1**	**Sun 25/2/2**	**Wed 25/1/1**	**Sun 25/2/2**	**Thu 25/1/16**	**Mon 25/2/17**	**15 days**		
64	Rebar Fixing [A]	NA	As Possible	25 days	Wed 25/1/1	Sat 25/1/25	Wed 25/1/1	Sat 25/1/25	Thu 25/1/16	Sun 25/2/9	15 days	0	62FS-17 days
65	Formwork Erection and Cast-in items	NA	As Possible	25 days	Thu 25/1/9	Sun 25/2/2	Thu 25/1/9	Sun 25/2/2	Fri 25/1/24	Mon 25/2/17	15 days	0	64FS-17 days
66	Concreting	NA	As Possible	1 day	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	Sat 25/2/1	Sat 25/2/1	15 days	0	65FS-17 days
67	**Walls**	NA	As Possible	**33 days**	**Sat 25/1/18**	**Wed 25/2/19**	**Sat 25/1/18**	**Wed 25/2/19**	**Sun 25/2/2**	**Thu 25/3/6**	**15 days**		
68	Rebar Fixing	NA	As Possible	25 days	Sat 25/1/18	Tue 25/2/11	Sat 25/1/18	Tue 25/2/11	Sun 25/2/2	Wed 25/2/26	15 days	0	66
69	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sun 25/1/26	Wed 25/2/19	Sun 25/1/26	Wed 25/2/19	Mon 25/2/10	Thu 25/3/6	15 days	0	68FS-17 days
70	Concreting	NA	As Possible	1 day	Mon 25/2/3	Mon 25/2/3	Mon 25/2/3	Mon 25/2/3	Tue 25/2/18	Tue 25/2/18	15 days	0	69FS-17 days
71	Backfilling and Compaction	NA	As Possible	10 days	Tue 25/2/4	Thu 25/2/13	Tue 25/2/4	Thu 25/2/13	Wed 25/2/19	Fri 25/2/28	15 days	0	70
72	Removal of Sheetpiles	NA	As Possible	10 days	Fri 25/2/7	Sun 25/2/16	Fri 25/2/7	Sun 25/2/16	Sat 25/2/22	Mon 25/3/3	15 days	0	71FS-7 days
73	Animal Escape Ramps	########	Later Than	21 days	Fri 25/1/31	Thu 25/2/20	Fri 25/1/31	Thu 25/2/20	Tue 26/9/15	Mon 26/10/5	592 days	0	72FS-17 days
74	Demolish & relocate retaining wall YLL796/A/5-6	NA	As Possible	30 days	Fri 25/1/31	Sat 25/3/1	Fri 25/1/31	Sat 25/3/1	Sat 25/2/15	Sun 25/3/16	15 days	0	72FS-17 days
75	Demolish & relocate AFCD Weir & pedestrian crossing	NA	As Possible	30 days	Fri 25/1/31	Sat 25/3/1	Fri 25/1/31	Sat 25/3/1	Sat 25/2/15	Sun 25/3/16	15 days	0	72FS-17 days
76	**LFT02 CH.A100.00~CH.A163.00**	NA	As Possible	**85 days**	**Mon 25/2/10**	**Mon 25/5/5**	**Mon 25/2/10**	**Mon 25/5/5**	**Tue 25/2/25**	**Tue 25/5/20**	**15 days**		
77	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Mon 25/2/10	Thu 25/3/6	Mon 25/2/10	Thu 25/3/6	Tue 25/2/25	Fri 25/3/21	15 days	0	74FS-20 days,7
78	Excavation and Lateral Support	NA	As Possible	25 days	Thu 25/2/20	Sun 25/3/16	Thu 25/2/20	Sun 25/3/16	Fri 25/3/7	Mon 25/3/31	15 days	0	77FS-15 days
79	**Ground and Edge Beams**	NA	As Possible	**33 days**	**Fri 25/2/28**	**Tue 25/4/1**	**Fri 25/2/28**	**Tue 25/4/1**	**Sat 25/3/15**	**Wed 25/4/16**	**15 days**		
80	Rebar Fixing	NA	As Possible	25 days	Fri 25/2/28	Mon 25/3/24	Fri 25/2/28	Mon 25/3/24	Sat 25/3/15	Tue 25/4/8	15 days	0	78FS-17 days
81	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sat 25/3/8	Tue 25/4/1	Sat 25/3/8	Tue 25/4/1	Sun 25/3/23	Wed 25/4/16	15 days	0	80FS-17 days
82	Concreting	NA	As Possible	1 day	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	Mon 25/3/31	Mon 25/3/31	15 days	0	81FS-17 days
83	**Walls**	NA	As Possible	**33 days**	**Mon 25/3/17**	**Fri 25/4/18**	**Mon 25/3/17**	**Fri 25/4/18**	**Tue 25/4/1**	**Sat 25/5/3**	**15 days**		
84	Rebar Fixing	NA	As Possible	25 days	Mon 25/3/17	Thu 25/4/10	Mon 25/3/17	Thu 25/4/10	Tue 25/4/1	Fri 25/4/25	15 days	0	82
85	Formwork Erection and Cast-in items	NA	As Possible	25 days	Tue 25/3/25	Fri 25/4/18	Tue 25/3/25	Fri 25/4/18	Wed 25/4/9	Sat 25/5/3	15 days	0	84FS-17 days
86	Concreting	NA	As Possible	1 day	Wed 25/4/2	Wed 25/4/2	Wed 25/4/2	Wed 25/4/2	Thu 25/4/17	Thu 25/4/17	15 days	0	85FS-17 days
87	Backfilling and Compaction	NA	As Possible	25 days	Thu 25/4/3	Sun 25/4/27	Thu 25/4/3	Sun 25/4/27	Fri 25/4/18	Mon 25/5/12	15 days	0	86
88	Removal of Sheetpiles	NA	As Possible	25 days	Fri 25/4/11	Mon 25/5/5	Fri 25/4/11	Mon 25/5/5	Sat 25/4/26	Tue 25/5/20	15 days	0	87FS-17 days
89	Pedestrian Crossing no. 2	NA	As Possible	21 days	Sat 25/4/19	Fri 25/5/9	Sat 25/4/19	Fri 25/5/9	Sat 27/3/13	Fri 27/4/2	693 days	3	88FS-17 days
90	Demolish & relocate retaining wall YLL796/A/14-15	NA	As Possible	30 days	Sat 25/4/19	Sun 25/5/18	Sat 25/4/19	Sun 25/5/18	Sun 25/5/4	Mon 25/6/2	15 days	0	88FS-17 days
91	**LFT08 CH.A300.75~CH.A391.0**	NA	As Possible	**92 days**	**Tue 25/4/29**	**Tue 25/7/29**	**Tue 25/4/29**	**Tue 25/7/29**	**Wed 25/5/14**	**Wed 25/8/13**	**15 days**		
92	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Tue 25/4/29	Fri 25/5/23	Tue 25/4/29	Fri 25/5/23	Wed 25/5/14	Sat 25/6/7	15 days	1	90FS-20 days
93	Excavation and Lateral Support	NA	As Possible	25 days	Fri 25/5/9	Mon 25/6/2	Fri 25/5/9	Mon 25/6/2	Sat 25/5/24	Tue 25/6/17	15 days	1	92FS-15 days
94	**Ground and Edge Beams**	NA	As Possible	**40 days**	**Sat 25/5/17**	**Wed 25/6/25**	**Sat 25/5/17**	**Wed 25/6/25**	**Sun 25/6/1**	**Thu 25/7/10**	**15 days**		
95	Install precast portion (ground beam)	NA	As Possible	28 days	Sat 25/5/17	Fri 25/6/13	Sat 25/5/17	Fri 25/6/13	Sun 25/6/1	Sat 25/6/28	15 days	0	93FS-17 days
96	Rebar Fixing	NA	As Possible	25 days	Sat 25/5/24	Tue 25/6/17	Sat 25/5/24	Tue 25/6/17	Sun 25/6/8	Wed 25/7/2	15 days	1	95FS-21 days
97	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sun 25/6/1	Wed 25/6/25	Sun 25/6/1	Wed 25/6/25	Mon 25/6/16	Thu 25/7/10	15 days	1	96FS-17 days
98	Concreting	NA	As Possible	1 day	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Tue 25/6/24	Tue 25/6/24	15 days	0	97FS-17 days
99	**Walls**	NA	As Possible	**33 days**	**Tue 25/6/10**	**Sat 25/7/12**	**Tue 25/6/10**	**Sat 25/7/12**	**Wed 25/6/25**	**Sun 25/7/27**	**15 days**		
100	Rebar Fixing	NA	As Possible	25 days	Tue 25/6/10	Fri 25/7/4	Tue 25/6/10	Fri 25/7/4	Wed 25/6/25	Sat 25/7/19	15 days	1	98
101	Formwork Erection and Cast-in items	NA	As Possible	25 days	Wed 25/6/18	Sat 25/7/12	Wed 25/6/18	Sat 25/7/12	Thu 25/7/3	Sun 25/7/27	15 days	1	100FS-17 days
102	Concreting	NA	As Possible	1 day	Thu 25/6/26	Thu 25/6/26	Thu 25/6/26	Thu 25/6/26	Fri 25/7/11	Fri 25/7/11	15 days	0	101FS-17 days
103	Backfilling and Compaction	NA	As Possible	25 days	Fri 25/6/27	Mon 25/7/21	Fri 25/6/27	Mon 25/7/21	Sat 25/7/12	Tue 25/8/5	15 days	0	102
104	Removal of Sheetpiles	NA	As Possible	25 days	Sat 25/7/5	Tue 25/7/29	Sat 25/7/5	Tue 25/7/29	Sun 25/7/20	Wed 25/8/13	15 days	0	103FS-17 days
105	Pedestrian Crossing no. 4	########	Later Than	21 days	Sun 25/7/13	Sat 25/8/2	Sun 25/7/13	Sat 25/8/2	Mon 25/7/28	Sun 25/8/17	15 days	3	104FS-17 days
106	Demolition of existing crossing	NA	As Possible	30 days	Thu 25/7/17	Fri 25/8/15	Thu 25/7/17	Fri 25/8/15	Fri 25/8/1	Sat 25/8/30	15 days	0	105FS-17 days
107	**LFT01 CH.A0.00~CH.A100.00 (PC1~PC2)**	NA	As Possible	**90 days**	**Sun 25/7/27**	**Fri 25/10/24**	**Sun 25/7/27**	**Fri 25/10/24**	**Mon 25/8/11**	**Sat 25/11/8**	**15 days**		
108	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Sun 25/7/27	Wed 25/8/20	Sun 25/7/27	Wed 25/8/20	Mon 25/8/11	Thu 25/9/4	15 days	1	106FS-20 days
109	Excavation and Lateral Support	NA	As Possible	25 days	Wed 25/8/6	Sat 25/8/30	Wed 25/8/6	Sat 25/8/30	Thu 25/8/21	Sun 25/9/14	15 days	1	108FS-15 days
110	**Ground and Edge Beams**	NA	As Possible	**40 days**	**Thu 25/8/14**	**Mon 25/9/22**	**Thu 25/8/14**	**Mon 25/9/22**	**Fri 25/8/29**	**Tue 25/10/7**	**15 days**		
111	Install precast portion (ground beam)	NA	As Possible	28 days	Thu 25/8/14	Wed 25/9/10	Thu 25/8/14	Wed 25/9/10	Fri 25/8/29	Thu 25/9/25	15 days	0	109FS-17 days
112	Rebar Fixing	NA	As Possible	25 days	Thu 25/8/21	Sun 25/9/14	Thu 25/8/21	Sun 25/9/14	Fri 25/9/5	Mon 25/9/29	15 days	1	111FS-21 days
113	Formwork Erection and Cast-in items	NA	As Possible	25 days	Fri 25/8/29	Mon 25/9/22	Fri 25/8/29	Mon 25/9/22	Sat 25/9/13	Tue 25/10/7	15 days	1	112FS-17 days
114	Concreting	NA	As Possible	1 day	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	Sun 25/9/21	Sun 25/9/21	15 days	0	113FS-17 days
115	**Walls**	NA	As Possible	**33 days**	**Sun 25/9/7**	**Thu 25/10/9**	**Sun 25/9/7**	**Thu 25/10/9**	**Mon 25/9/22**	**Fri 25/10/24**	**15 days**		

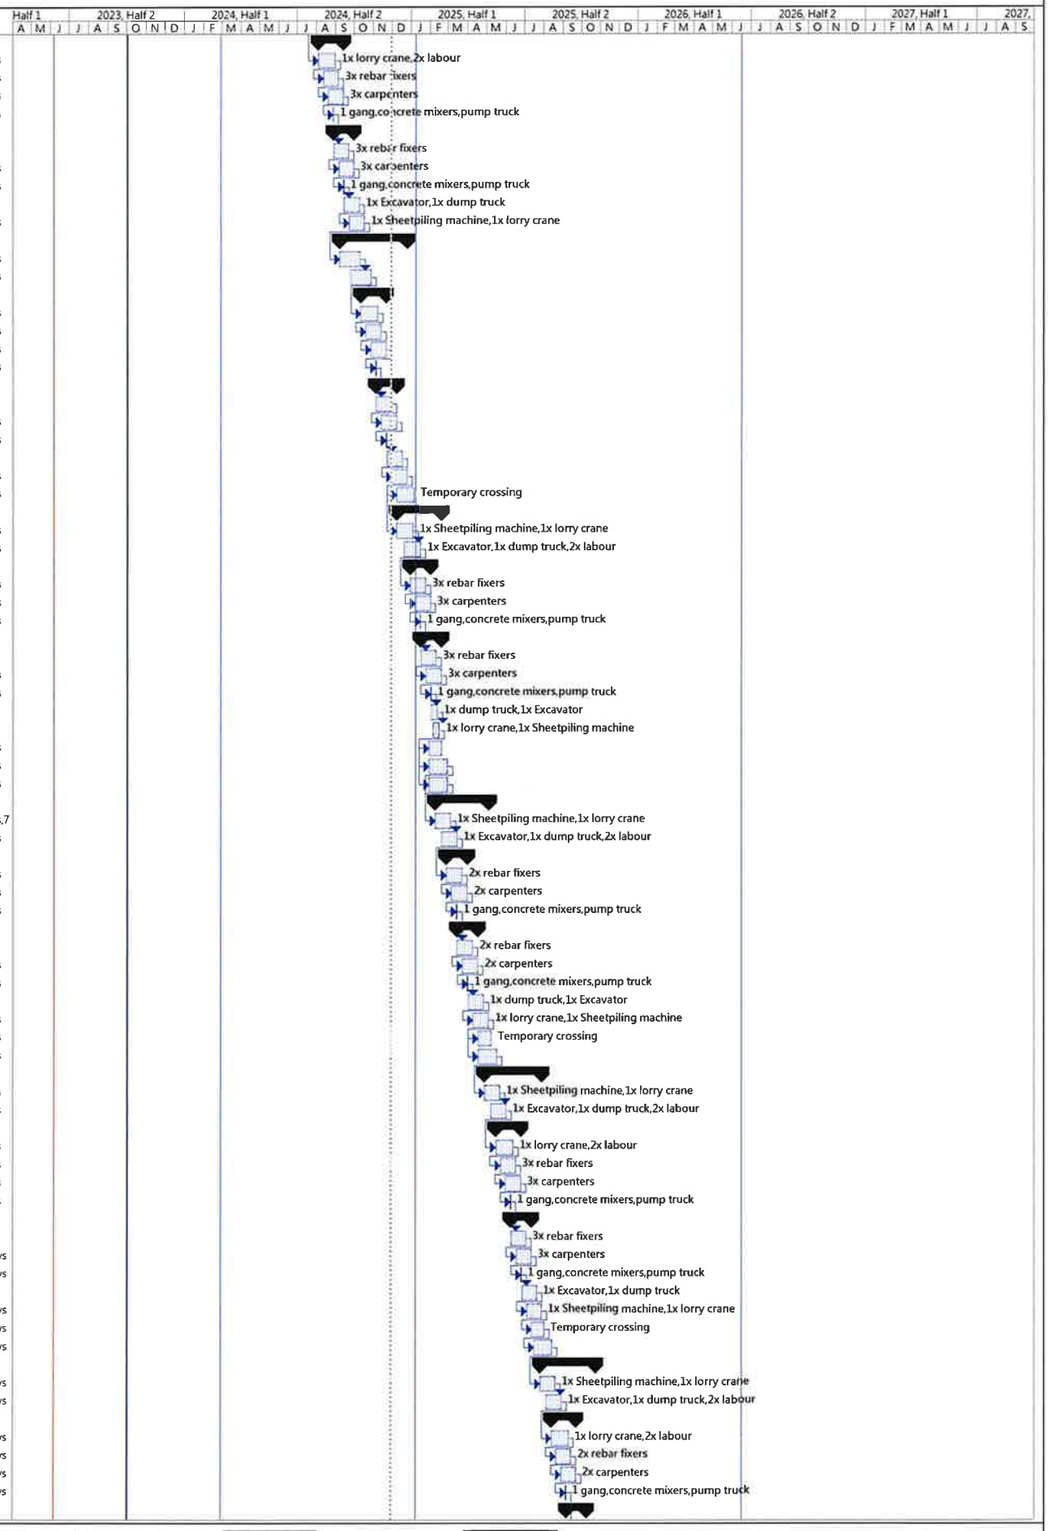


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
116	Rebar Fixing	NA	As Possible	25 days	Sun 25/9/7	Wed 25/10/1	Sun 25/9/7	Wed 25/10/1	Mon 25/9/22	Thu 25/10/16	15 days	1	114
117	Formwork Erection and Cast-in items	NA	As Possible	25 days	Mon 25/9/15	Thu 25/10/9	Mon 25/9/15	Thu 25/10/9	Tue 25/9/30	Fri 25/10/24	15 days	1	116FS-17 days
118	Concreting	NA	As Possible	1 day	Tue 25/9/23	Tue 25/9/23	Tue 25/9/23	Tue 25/9/23	Wed 25/10/8	Wed 25/10/8	15 days	0	117FS-17 days
119	Backfilling and Compaction	NA	As Possible	24 days	Wed 25/9/24	Fri 25/10/17	Wed 25/9/24	Fri 25/10/17	Thu 25/10/9	Sat 25/11/1	15 days	0	118
120	Removal of Sheetpiles	NA	As Possible	24 days	Wed 25/10/1	Fri 25/10/24	Wed 25/10/1	Fri 25/10/24	Thu 25/10/16	Sat 25/11/8	15 days	0	119FS-17 days
121	Pedestrian Crossing no. 1	########	Later Than	21 days	Wed 25/10/8	Tue 25/10/28	Wed 25/10/8	Tue 25/10/28	Thu 25/10/23	Wed 25/11/12	15 days	0	120FS-17 days
122	Demolish & relocate retaining wall YLL796/A/20-22	NA	As Possible	30 days	Sun 25/10/12	Mon 25/11/10	Sun 25/10/12	Mon 25/11/10	Mon 25/10/27	Tue 25/11/25	15 days	0	121FS-17 days
123	**LFT09 CH.A391.00~CH.A464.00**	**NA**	**As Possible**	**92 days**	**Wed 25/10/22**	**Wed 26/1/21**	**Wed 25/10/22**	**Wed 26/1/21**	**Thu 25/11/6**	**Thu 26/2/5**	15 days		
124	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Wed 25/10/22	Sat 25/11/15	Wed 25/10/22	Sat 25/11/15	Thu 25/11/6	Sun 25/11/30	15 days	1	122FS-20 days
125	Excavation and Lateral Support	NA	As Possible	25 days	Sat 25/11/1	Tue 25/11/25	Sat 25/11/1	Tue 25/11/25	Sun 25/11/16	Wed 25/12/10	15 days	1	124FS-15 days
126	**Ground and Edge Beams**	**NA**	**As Possible**	**40 days**	**Sun 25/11/9**	**Thu 25/12/18**	**Sun 25/11/9**	**Thu 25/12/18**	##########	**Fri 26/1/2**	15 days		
127	Install precast portion (ground beam)	NA	As Possible	28 days	Sun 25/11/9	Sat 25/12/6	Sun 25/11/9	Sat 25/12/6	Mon 25/11/24	Sun 25/12/21	15 days	0	125FS-17 days
128	Rebar Fixing	NA	As Possible	25 days	Sun 25/11/16	Wed 25/12/10	Sun 25/11/16	Wed 25/12/10	Mon 25/12/1	Thu 25/12/25	15 days	1	127FS-21 days
129	Formwork Erection and Cast-in items	NA	As Possible	25 days	Mon 25/11/24	Thu 25/12/18	Mon 25/11/24	Thu 25/12/18	Tue 25/12/9	Fri 26/1/2	15 days	1	128FS-17 days
130	Concreting	NA	As Possible	1 day	Tue 25/12/2	Tue 25/12/2	Tue 25/12/2	Tue 25/12/2	Wed 25/12/17	Wed 25/12/17	15 days	0	129FS-17 days
131	**Walls**	**NA**	**As Possible**	**33 days**	**Wed 25/12/3**	**Sun 26/1/4**	**Wed 25/12/3**	**Sun 26/1/4**	**Thu 25/12/18**	**Mon 26/1/19**	15 days		
132	Rebar Fixing	NA	As Possible	25 days	Wed 25/12/3	Sat 25/12/27	Wed 25/12/3	Sat 25/12/27	Thu 25/12/18	Sun 26/1/11	15 days	1	130
133	Formwork Erection and Cast-in items	NA	As Possible	25 days	Thu 25/12/11	Sun 26/1/4	Thu 25/12/11	Sun 26/1/4	Fri 25/12/26	Mon 26/1/19	15 days	1	132FS-17 days
134	Concreting	NA	As Possible	1 day	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	Sat 26/1/3	Sat 26/1/3	15 days	0	133FS-17 days
135	Backfilling and Compaction	NA	As Possible	25 days	Sat 25/12/20	Tue 26/1/13	Sat 25/12/20	Tue 26/1/13	Sun 26/1/4	Wed 26/1/28	15 days	0	134
136	Removal of Sheetpiles	NA	As Possible	25 days	Sun 25/12/28	Wed 26/1/21	Sun 25/12/28	Wed 26/1/21	Mon 26/1/12	Thu 26/2/5	15 days	0	135FS-17 days
137	Pedestrian & Vehicular Crossing no. 3	NA	As Possible	28 days	Mon 26/1/5	Sun 26/2/1	Mon 26/1/5	Sun 26/2/1	Tue 26/1/20	Mon 26/2/16	15 days	4	136FS-17 days
138	**LFT10 CH.A464.00~CH.A554.00**	**NA**	**As Possible**	**92 days**	**Mon 26/1/12**	**Mon 26/4/13**	**Mon 26/1/12**	**Mon 26/4/13**	**Tue 26/1/27**	**Tue 26/4/28**	15 days		
139	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Mon 26/1/12	Thu 26/2/5	Mon 26/1/12	Thu 26/2/5	Tue 26/1/27	Fri 26/2/20	15 days	1	137FS-21 days
140	Excavation and Lateral Support	NA	As Possible	25 days	Thu 26/1/22	Sun 26/2/15	Thu 26/1/22	Sun 26/2/15	Fri 26/2/6	Mon 26/3/2	15 days	1	139FS-15 days
141	**Ground and Edge Beams**	**NA**	**As Possible**	**40 days**	**Fri 26/1/30**	**Tue 26/3/10**	**Fri 26/1/30**	**Tue 26/3/10**	**Sat 26/2/14**	**Wed 26/3/25**	15 days		
142	Install precast portion (ground beam)	NA	As Possible	28 days	Fri 26/1/30	Thu 26/2/26	Fri 26/1/30	Thu 26/2/26	Sat 26/2/14	Fri 26/3/13	15 days	0	140FS-17 days
143	Rebar Fixing	NA	As Possible	25 days	Fri 26/2/6	Mon 26/3/2	Fri 26/2/6	Mon 26/3/2	Sat 26/2/21	Tue 26/3/17	15 days	1	142FS-21 days
144	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sat 26/2/14	Tue 26/3/10	Sat 26/2/14	Tue 26/3/10	Sun 26/3/1	Wed 26/3/25	15 days	1	143FS-17 days
145	Concreting	NA	As Possible	1 day	Sun 26/2/22	Sun 26/2/22	Sun 26/2/22	Sun 26/2/22	Mon 26/3/9	Mon 26/3/9	15 days	0	144FS-17 days
146	**Walls**	**NA**	**As Possible**	**33 days**	**Mon 26/2/23**	**Fri 26/3/27**	**Mon 26/2/23**	**Fri 26/3/27**	**Tue 26/3/10**	**Sat 26/4/11**	15 days		
147	Rebar Fixing	NA	As Possible	25 days	Mon 26/2/23	Thu 26/3/19	Mon 26/2/23	Thu 26/3/19	Tue 26/3/10	Fri 26/4/3	15 days	1	145
148	Formwork Erection and Cast-in items	NA	As Possible	25 days	Tue 26/3/3	Fri 26/3/27	Tue 26/3/3	Fri 26/3/27	Wed 26/3/18	Sat 26/4/11	15 days	1	147FS-17 days
149	Concreting	NA	As Possible	1 day	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	Thu 26/3/26	Thu 26/3/26	15 days	0	148FS-17 days
150	Backfilling and Compaction	NA	As Possible	25 days	Thu 26/3/12	Sun 26/4/5	Thu 26/3/12	Sun 26/4/5	Fri 26/3/27	Mon 26/4/20	15 days	0	149
151	Removal of Sheetpiles	NA	As Possible	25 days	Fri 26/3/20	Mon 26/4/13	Fri 26/3/20	Mon 26/4/13	Sat 26/4/4	Tue 26/4/28	15 days	0	150FS-17 days
152	Pedestnan & Vehicular Crossing no. 4	########	Later Than	28 days	Sat 26/3/28	Fri 26/4/24	Sat 26/3/28	Fri 26/4/24	Tue 26/9/8	Mon 26/10/5	164 days	4	151FS-17 days
153	Protection to ex. Dongjiang Water Main	NA	As Possible	10 days	Sat 26/3/28	Mon 26/4/6	Sat 26/3/28	Mon 26/4/6	Sun 26/4/12	Tue 26/4/21	15 days	0	151FS-17 days
154	**LFT11 CH.A554.00~CH.A700.00**	**NA**	**As Possible**	**92 days**	**Tue 26/4/7**	**Tue 26/7/7**	**Tue 26/4/7**	**Tue 26/7/7**	**Wed 26/4/22**	**Wed 26/7/22**	15 days		
155	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	30 days	Tue 26/4/7	Wed 26/5/6	Tue 26/4/7	Wed 26/5/6	Wed 26/4/22	Thu 26/5/21	15 days	1	153
156	Excavation and Lateral Support	NA	As Possible	30 days	Sun 26/4/19	Mon 26/5/18	Sun 26/4/19	Mon 26/5/18	Mon 26/5/4	Tue 26/6/2	15 days	1	155FS-18 days
157	**Ground and Edge Beams**	**NA**	**As Possible**	**40 days**	**Wed 26/4/29**	**Sun 26/6/7**	**Wed 26/4/29**	**Sun 26/6/7**	**Thu 26/5/14**	**Mon 26/6/22**	15 days		
158	Install precast portion (ground beam)	NA	As Possible	28 days	Wed 26/4/29	Tue 26/5/26	Wed 26/4/29	Tue 26/5/26	Thu 26/5/14	Wed 26/6/10	15 days	0	156FS-20 days
159	Rebar Fixing	NA	As Possible	25 days	Wed 26/5/6	Sat 26/5/30	Wed 26/5/6	Sat 26/5/30	Thu 26/5/21	Sun 26/6/14	15 days	1	158FS-21 days
160	Formwork Erection and Cast-in items	NA	As Possible	25 days	Thu 26/5/14	Sun 26/6/7	Thu 26/5/14	Sun 26/6/7	Fri 26/5/29	Mon 26/6/22	15 days	1	159FS-17 days
161	Concreting	NA	As Possible	1 day	Fri 26/5/22	Fri 26/5/22	Fri 26/5/22	Fri 26/5/22	Sat 26/6/6	Sat 26/6/6	15 days	0	160FS-17 days
162	**Walls**	**NA**	**As Possible**	**33 days**	**Sat 26/5/23**	**Wed 26/6/24**	**Sat 26/5/23**	**Wed 26/6/24**	**Sun 26/6/7**	**Thu 26/7/9**	15 days		
163	Rebar Fixing	NA	As Possible	25 days	Sat 26/5/23	Tue 26/6/16	Sat 26/5/23	Tue 26/6/16	Sun 26/6/7	Wed 26/7/1	15 days	1	161
164	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sun 26/5/31	Wed 26/6/24	Sun 26/5/31	Wed 26/6/24	Mon 26/6/15	Thu 26/7/9	15 days	1	163FS-17 days
165	Concreting	NA	As Possible	1 day	Mon 26/6/8	Mon 26/6/8	Mon 26/6/8	Mon 26/6/8	Tue 26/6/23	Tue 26/6/23	15 days	0	164FS-17 days
166	Backfilling and Compaction	NA	As Possible	25 days	Tue 26/6/9	Fri 26/7/3	Tue 26/6/9	Fri 26/7/3	Wed 26/6/24	Sat 26/7/18	15 days	0	165
167	Removal of Sheetpiles	NA	As Possible	25 days	Sat 26/6/13	Tue 26/7/7	Sat 26/6/13	Tue 26/7/7	Sun 26/6/28	Wed 26/7/22	15 days	0	166FS-21 days
168	**LFT12 CH.A700.00~CH.A818.86**	**NA**	**As Possible**	**92 days**	**Wed 26/6/17**	**Wed 26/9/16**	**Wed 26/6/17**	**Wed 26/9/16**	**Thu 26/7/2**	**Thu 26/10/1**	15 days		
169	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Wed 26/6/17	Sat 26/7/11	Wed 26/6/17	Sat 26/7/11	Thu 26/7/2	Sun 26/7/26	15 days	1	167FS-21 days,
170	Excavation and Lateral Support	NA	As Possible	25 days	Sat 26/6/27	Tue 26/7/21	Sat 26/6/27	Tue 26/7/21	Sun 26/7/12	Wed 26/8/5	15 days	1	169FS-15 days
171	**Ground and Edge Beams**	**NA**	**As Possible**	**40 days**	**Sun 26/7/5**	**Thu 26/8/13**	**Sun 26/7/5**	**Thu 26/8/13**	**Mon 26/7/20**	**Fri 26/8/28**	15 days		
172	Install precast portion (ground beam)	NA	As Possible	28 days	Sun 26/7/5	Sat 26/8/1	Sun 26/7/5	Sat 26/8/1	Mon 26/7/20	Sun 26/8/16	15 days	0	170FS-17 days
173	Rebar Fixing	NA	As Possible	25 days	Sun 26/7/12	Wed 26/8/5	Sun 26/7/12	Wed 26/8/5	Mon 26/7/27	Thu 26/8/20	15 days	1	172FS-21 days
174	Formwork Erection and Cast-in items	NA	As Possible	25 days	Mon 26/7/20	Thu 26/8/13	Mon 26/7/20	Thu 26/8/13	Tue 26/8/4	Fri 26/8/28	15 days	1	173FS-17 days
175	Concreting	NA	As Possible	1 day	Tue 26/7/28	Tue 26/7/28	Tue 26/7/28	Tue 26/7/28	Wed 26/8/12	Wed 26/8/12	15 days	0	174FS-17 days
176	**Walls**	**NA**	**As Possible**	**33 days**	**Wed 26/7/29**	**Sun 26/8/30**	**Wed 26/7/29**	**Sun 26/8/30**	**Thu 26/8/13**	**Mon 26/9/14**	15 days		
177	Rebar Fixing	NA	As Possible	25 days	Wed 26/7/29	Sat 26/8/22	Wed 26/7/29	Sat 26/8/22	Thu 26/8/13	Sun 26/9/6	15 days	1	175
178	Formwork Erection and Cast-in items	NA	As Possible	25 days	Thu 26/8/6	Sun 26/8/30	Thu 26/8/6	Sun 26/8/30	Fri 26/8/21	Mon 26/9/14	15 days	1	177FS-17 days
179	Concreting	NA	As Possible	1 day	Fri 26/8/14	Fri 26/8/14	Fri 26/8/14	Fri 26/8/14	Sat 26/8/29	Sat 26/8/29	15 days	0	178FS-17 days
180	Backfilling and Compaction	NA	As Possible	25 days	Sat 26/8/15	Tue 26/9/8	Sat 26/8/15	Tue 26/9/8	Sun 26/8/30	Wed 26/9/23	15 days	0	179
181	Removal of Sheetpiles	NA	As Possible	25 days	Sun 26/8/23	Wed 26/9/16	Sun 26/8/23	Wed 26/9/16	Mon 26/9/7	Thu 26/10/1	15 days	0	180FS-17 days
182	Relocate Septic Tank & Soakaway Pit	NA	As Possible	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Tue 26/9/15	Mon 26/10/5	15 days	4	181FS-17 days
183	Animal Escape Ramp	NA	As Possible	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Sat 27/3/13	Fri 27/4/2	194 days	0	182FS-21 days
184	U-channels	########	Later Than	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Tue 26/9/15	Mon 26/10/5	15 days	0	182FS-21 days
185	Facing stone	########	Later Than	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Tue 26/9/15	Mon 26/10/5	15 days	0	182FS-21 days
186	ABWF works	########	Later Than	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Tue 26/9/15	Mon 26/10/5	15 days	0	182FS-21 days
187	Bedding works	########	Later Than	21 days	Mon 26/8/31	Sun 26/9/20	Mon 26/8/31	Sun 26/9/20	Tue 26/9/15	Mon 26/10/5	15 days	0	182FS-21 days
188													
189	**LFT04 CH.B51.00~CH.B149.77**	**NA**	**As Possible**	**87 days**	**Thu 25/1/2**	**Sat 25/3/29**	**Thu 25/1/2**	**Sat 25/3/29**	**Thu 26/4/30**	**Sat 26/7/25**	**483 days**		
190	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Thu 25/1/2	Sun 25/1/26	Thu 25/1/2	Sun 25/1/26	Thu 26/4/30	Sun 26/5/24	483 days	0	20
191	Excavation and Lateral Support	NA	As Possible	25 days	Sun 25/1/12	Wed 25/2/5	Sun 25/1/12	Wed 25/2/5	Sun 26/5/10	Wed 26/6/3	483 days	0	190FS-15 days
192	**Ground and Edge Beams**	**NA**	**As Possible**	**33 days**	**Mon 25/1/20**	**Fri 25/2/21**	**Mon 25/1/20**	**Fri 25/2/21**	**Mon 26/5/18**	**Fri 26/6/19**	**483 days**		
193	Rebar Fixing	NA	As Possible	25 days	Mon 25/1/20	Thu 25/2/13	Mon 25/1/20	Thu 25/2/13	Mon 26/5/18	Thu 26/6/11	483 days	0	191FS-17 days
194	Formwork Erection and Cast-in items	NA	As Possible	25 days	Tue 25/1/28	Fri 25/2/21	Tue 25/1/28	Fri 25/2/21	Tue 26/5/26	Fri 26/6/19	483 days	0	193FS-17 days
195	Concreting	NA	As Possible	1 day	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	Fri 26/6/5	Fri 26/6/5	483 days	0	194FS-15 days
196	**Walls**	**NA**	**As Possible**	**33 days**	**Sat 25/2/8**	**Wed 25/3/12**	**Sat 25/2/8**	**Wed 25/3/12**	**Sat 26/6/6**	**Wed 26/7/8**	**483 days**		
197	Rebar Fixing	NA	As Possible	25 days	Sat 25/2/8	Tue 25/3/4	Sat 25/2/8	Tue 25/3/4	Sat 26/6/6	Tue 26/6/30	483 days	0	195

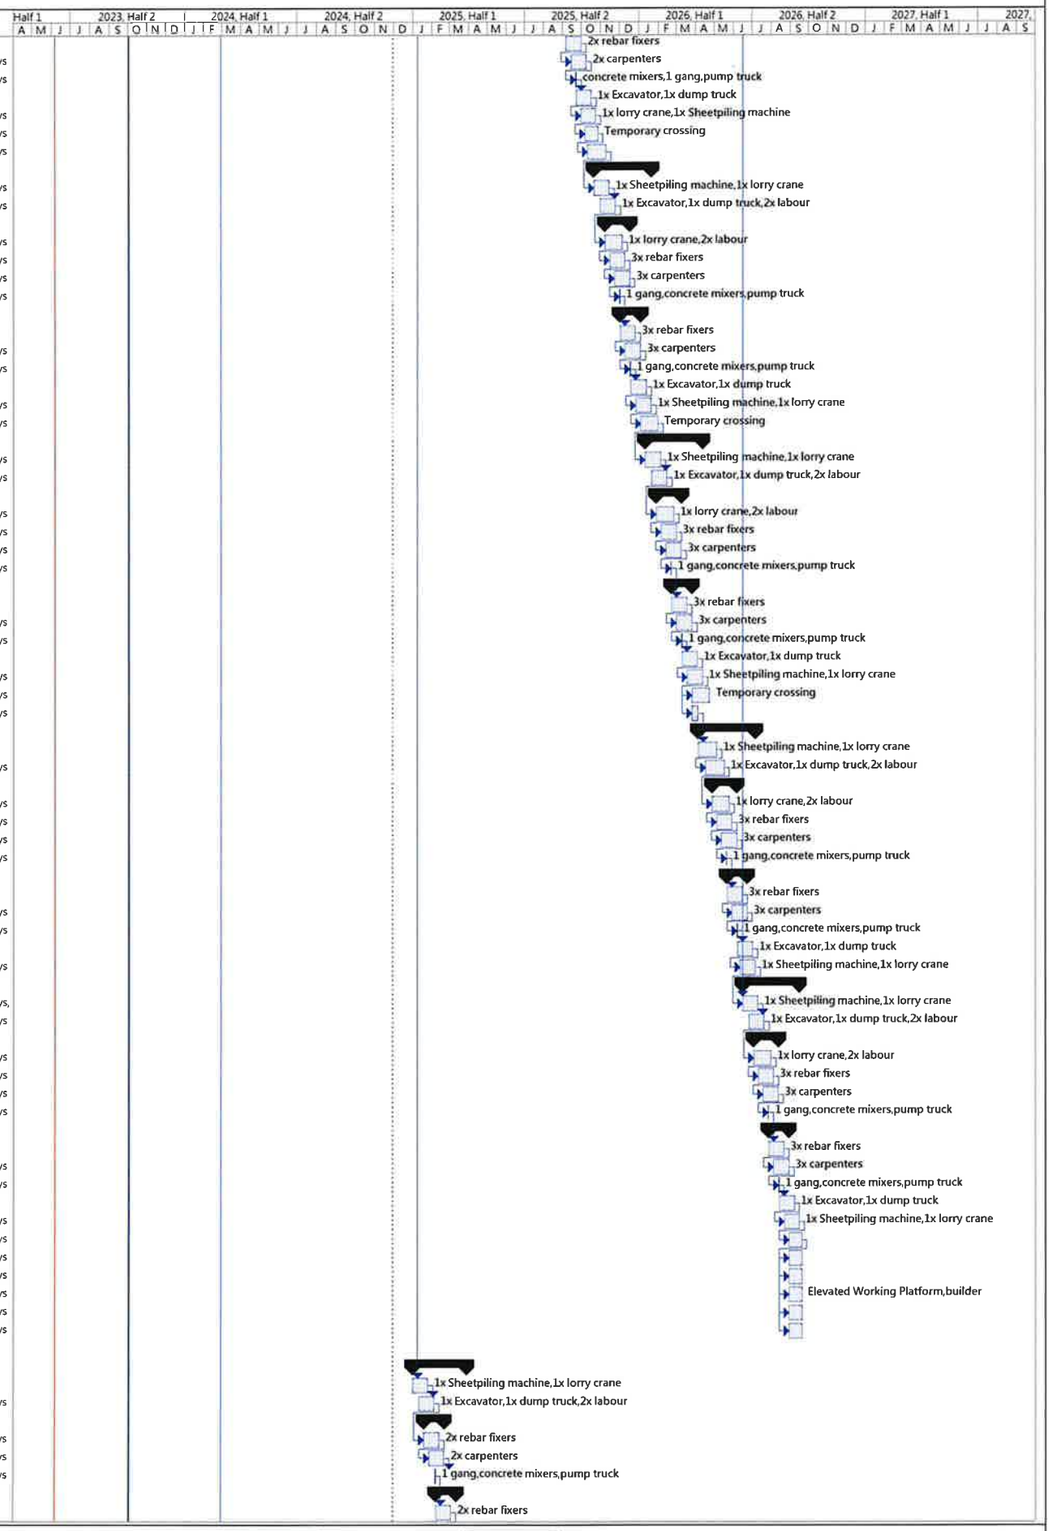


Revision.: 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
198	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sun 25/2/16	Wed 25/3/12	Sun 25/2/16	Wed 25/3/12	Sun 26/6/14	Wed 26/7/8	483 days	0	197FS-17 days
199	Concreting	NA	As Possible	1 day	Mon 25/2/24	Mon 25/2/24	Mon 25/2/24	Mon 25/2/24	Mon 26/6/22	Mon 26/6/22	483 days	0	198FS-17 days
200	Backfilling and Compaction	NA	As Possible	25 days	Tue 25/2/25	Fri 25/3/21	Tue 25/2/25	Fri 25/3/21	Tue 26/6/23	Fri 26/7/17	483 days	0	199
201	Removal of Sheetpiles	NA	As Possible	25 days	Wed 25/3/5	Sat 25/3/29	Wed 25/3/5	Sat 25/3/29	Wed 26/7/1	Sat 26/7/25	483 days	0	200FS-17 days
202	**LFT03 CH.B0.00~CH.B51.00 (PC3)**	**NA**	**As Possible**	**85 days**	**Thu 25/3/13**	**Thu 25/6/5**	**Thu 25/3/13**	**Thu 25/6/5**	**Thu 26/7/9**	**Thu 26/10/1**	**483 days**		
203	Temp. Drainage Diversion / Sheetpiling	NA	As Possible	25 days	Thu 25/3/13	Sun 25/4/6	Thu 25/3/13	Sun 25/4/6	Thu 26/7/9	Sun 26/8/2	483 days	1	201FS-17 days
204	Excavation and Lateral Support	NA	As Possible	25 days	Sun 25/3/23	Wed 25/4/16	Sun 25/3/23	Wed 25/4/16	Sun 26/7/19	Wed 26/8/12	483 days	1	203FS-15 days
205	**Ground and Edge Beams**	**NA**	**As Possible**	**33 days**	**Mon 25/3/31**	**Fri 25/5/2**	**Mon 25/3/31**	**Fri 25/5/2**	**Mon 26/7/27**	**Fri 26/8/28**	**483 days**		
206	Rebar Fixing	NA	As Possible	25 days	Mon 25/3/31	Thu 25/4/24	Mon 25/3/31	Thu 25/4/24	Mon 26/7/27	Thu 26/8/20	483 days	1	204FS-17 days
207	Formwork Erection and Cast-in items	NA	As Possible	25 days	Tue 25/4/8	Fri 25/5/2	Tue 25/4/8	Fri 25/5/2	Tue 26/8/4	Fri 26/8/28	483 days	1	206FS-17 days
208	Concreting	NA	As Possible	1 day	Wed 25/4/16	Wed 25/4/16	Wed 25/4/16	Wed 25/4/16	Wed 26/8/12	Wed 26/8/12	483 days	0	207FS-17 days
209	**Walls**	**NA**	**As Possible**	**33 days**	**Thu 25/4/17**	**Mon 25/5/19**	**Thu 25/4/17**	**Mon 25/5/19**	**Thu 26/8/13**	**Mon 26/9/14**	**483 days**		
210	Rebar Fixing	NA	As Possible	25 days	Thu 25/4/17	Sun 25/5/11	Thu 25/4/17	Sun 25/5/11	Thu 26/8/13	Sun 26/9/6	483 days	1	208
211	Formwork Erection and Cast-in items	NA	As Possible	25 days	Fri 25/4/25	Mon 25/5/19	Fri 25/4/25	Mon 25/5/19	Fri 26/8/21	Mon 26/9/14	483 days	1	210FS-17 days
212	Concreting	NA	As Possible	1 day	Sat 25/5/3	Sat 25/5/3	Sat 25/5/3	Sat 25/5/3	Sat 26/8/29	Sat 26/8/29	483 days	0	211FS-17 days
213	Backfilling and Compaction	NA	As Possible	25 days	Sun 25/5/4	Wed 25/5/28	Sun 25/5/4	Wed 25/5/28	Sun 26/8/30	Wed 26/9/23	483 days	0	212
214	Removal of Sheetpiles	NA	As Possible	25 days	Mon 25/5/12	Thu 25/6/5	Mon 25/5/12	Thu 25/6/5	Mon 26/9/7	Thu 26/10/1	483 days	0	213FS-17 days
215	Pedestrian Crossing no. 3	########	Later Than	21 days	Tue 25/5/20	Mon 25/6/9	Tue 25/5/20	Mon 25/6/9	Tue 26/9/15	Mon 26/10/5	483 days	3	214FS-17 days
110													
111	**Section VI**	**NA**	**As Possible**	**1075 days**	**Mon 23/5/15**	**Thu 26/4/23**	**Mon 23/5/15**	**Thu 26/4/23**	**Mon 23/5/29**	**Thu 26/4/23**	**0 days**		
2	access date of Portion C3	NA	As Possible	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	0 days	0	\\WingTatNasC
3	section VI (Lin Fa Tei - Kam Sheung Road)	Tue 25/8/26	Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days	0	\\WingTatNasC
4	Planned Completion Day	Thu 26/4/23	Later Than	240 days	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	Wed 25/8/27	Thu 26/4/23	0 days	0	3
5	**Site Establishment**	**NA**	**As Possible**	**868 days**	**Mon 23/5/15**	**Sun 25/9/28**	**Mon 23/5/15**	**Sun 25/9/28**	**Thu 23/10/12**	**Thu 26/4/23**	**150 days**		
6	Prepare and Accept Temp. Works Design and Method Statement [A]	NA	As Possible	734 days	Tue 23/9/26	Sun 25/9/28	Tue 23/9/26	Sun 25/9/28	Fri 24/2/23	Wed 26/2/25	150 days	0	\\WingTatNasC
7	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	194 days	Tue 23/9/12	Sat 24/3/23	Tue 23/9/12	Sat 24/3/23	Tue 23/11/21	Sat 24/6/1	70 days	0	\\WingTatNasC
8	Initial Survey [A]	NA	As Possible	868 days	Mon 23/5/15	Sun 25/9/28	Mon 23/5/15	Sun 25/9/28	Thu 23/10/12	Wed 26/2/25	150 days	0	
10	Initial Safety & Environmental measures	Thu 26/4/23	Later Than	60 days	Thu 24/1/4	Mon 24/3/4	Thu 24/1/4	Mon 24/3/4	Mon 26/2/23	Thu 26/4/23	781 days	0	15SF
12	Setup of instrumentation and monitoring	Thu 26/4/23	Later Than	25 days	Thu 24/2/8	Mon 24/3/4	Thu 24/2/8	Mon 24/3/4	Mon 26/3/30	Thu 26/4/23	781 days	0	15SF
13	Tree Survey	Thu 26/4/23	Later Than	25 days	Thu 24/2/8	Mon 24/3/4	Thu 24/2/8	Mon 24/3/4	Mon 26/3/30	Thu 26/4/23	781 days	0	15SF
14	UU detection	Thu 26/4/23	Later Than	25 days	Thu 24/2/8	Mon 24/3/4	Thu 24/2/8	Mon 24/3/4	Mon 26/3/30	Thu 26/4/23	781 days	0	15SF
15	[NCExxx] [PMI-030] Difficulty/infeasibility for construction of 1650mm dia. pipe at Kam Sheung Road (impact to be ascertained)	Mon 24/3/4	Start No Earlier Than	270 days	Mon 24/3/4	Thu 24/11/28	Mon 24/3/4	Thu 24/11/28	Mon 24/3/4	Thu 24/11/28	0 days	0	
16	**Temporary Traffic Arrangement**	**NA**	**As Possible**	**550 days**	**Mon 23/5/29**	**Thu 24/11/28**	**Mon 23/5/29**	**Thu 24/11/28**	**Mon 23/5/29**	**Thu 24/11/28**	**0 days**		
17	Application of XP [A]	NA	As Possible	400 days	Mon 23/5/29	Mon 24/7/1	Mon 23/5/29	Mon 24/7/1	Mon 23/5/29	Mon 24/7/1	0 days	0	2FS-1 day
18	Submission of TTA and Arrange TMLG [A]	NA	As Possible	370 days	Mon 23/5/29	Sat 24/6/1	Mon 23/5/29	Sat 24/6/1	Mon 23/5/29	Sat 24/6/1	0 days	0	2FS-1 day
19	Approval of TTA [A]	NA	As Possible	30 days	Sun 24/6/2	Mon 24/7/1	Sun 24/6/2	Mon 24/7/1	Sun 24/6/2	Mon 24/7/1	0 days	0	17FF,18,7
20	[NCExxx] [PMI-030] Submission of revised TTA and Arrange TMLG	NA	As Possible	120 days	Tue 24/7/2	Tue 24/10/29	Tue 24/7/2	Tue 24/10/29	Tue 24/7/2	Tue 24/10/29	0 days	0	19
21	[NCExxx] [PMI-030] Approval of revised TTA	NA	As Possible	30 days	Wed 24/10/30	Thu 24/11/28	Wed 24/10/30	Thu 24/11/28	Wed 24/10/30	Thu 24/11/28	0 days	0	20
22	**Drain Laying Works**	**NA**	**As Possible**	**661 days**	**Tue 24/7/2**	**Thu 26/4/23**	**Tue 24/7/2**	**Thu 26/4/23**	**Mon 24/9/30**	**Thu 26/4/23**	**0 days**		
23	Inspection Pit	NA	As Possible	60 days	Tue 24/7/2	Fri 24/8/30	Tue 24/7/2	Fri 24/8/30	Mon 24/9/30	Thu 24/11/28	90 days	0	19
24	[NCExxx] [PMI-030] Procurement, sampling and testing of drain pipes	NA	As Possible	60 days	Mon 24/9/30	Thu 24/11/28	Mon 24/9/30	Thu 24/11/28	Mon 24/9/30	Thu 24/11/28	0 days	0	15FS-60 days
25	**LFT.D3a~LFT.D4,1650PC,B,L=22.88,D=3.418**	**NA**	**As Possible**	**47 days**	**Fri 24/11/29**	**Tue 25/1/14**	**Fri 24/11/29**	**Tue 25/1/14**	**Fri 24/11/29**	**Tue 25/1/14**	**0 days**		
26	TTA Implementation	NA	As Possible	2 days	Fri 24/11/29	Sat 24/11/30	Fri 24/11/29	Sat 24/11/30	Fri 24/11/29	Sat 24/11/30	0 days	0	15,21,23,24
27	Breaking Ground	NA	As Possible	8 days	Fri 24/11/29	Fri 24/12/6	Fri 24/11/29	Fri 24/12/6	Fri 24/11/29	Fri 24/12/6	0 days	0	26FS-2 days
28	Excavation and Lateral Support	NA	As Possible	10 days	Thu 24/12/5	Sat 24/12/14	Thu 24/12/5	Sat 24/12/14	Thu 24/12/5	Sat 24/12/14	0 days	2	27FS-2 days
29	Drain Laying	NA	As Possible	10 days	Fri 24/12/13	Sun 24/12/22	Fri 24/12/13	Sun 24/12/22	Fri 24/12/13	Sun 24/12/22	0 days	2	28FS-2 days
30	Bedding and Backfilling	NA	As Possible	8 days	Sat 24/12/21	Sat 24/12/28	Sat 24/12/21	Sat 24/12/28	Sat 24/12/21	Sat 24/12/28	0 days	0	29FS-2 days
31	Manhole Construction	NA	As Possible	10 days	Fri 24/12/27	Sun 25/1/5	Fri 24/12/27	Sun 25/1/5	Fri 24/12/27	Sun 25/1/5	0 days	2	30FS-2 days
32	Reinstatement	NA	As Possible	8 days	Mon 25/1/6	Mon 25/1/13	Mon 25/1/6	Mon 25/1/13	Mon 25/1/6	Mon 25/1/13	0 days	0	31
33	TTA Removal	NA	As Possible	1 day	Tue 25/1/14	Tue 25/1/14	Tue 25/1/14	Tue 25/1/14	Tue 25/1/14	Tue 25/1/14	0 days	0	32
34	**LFT.D4~LFT.D5,1650PC,B,L=50.95,D=3.417**	**NA**	**As Possible**	**91 days**	**Wed 25/1/15**	**Tue 25/4/15**	**Wed 25/1/15**	**Tue 25/4/15**	**Wed 25/1/15**	**Tue 25/4/15**	**0 days**		
35	**Stage 1**	**NA**	**As Possible**	**52 days**	**Wed 25/1/15**	**Fri 25/3/7**	**Wed 25/1/15**	**Fri 25/3/7**	**Wed 25/1/15**	**Fri 25/3/7**	**0 days**		
36	TTA Implementation	NA	As Possible	2 days	Wed 25/1/15	Thu 25/1/16	Wed 25/1/15	Thu 25/1/16	Wed 25/1/15	Thu 25/1/16	0 days	0	33
37	Breaking Ground	NA	As Possible	10 days	Wed 25/1/15	Fri 25/1/24	Wed 25/1/15	Fri 25/1/24	Wed 25/1/15	Fri 25/1/24	0 days	2	36FS-2 days
38	Excavation and Lateral Support	NA	As Possible	12 days	Thu 25/1/23	Mon 25/2/3	Thu 25/1/23	Mon 25/2/3	Thu 25/1/23	Mon 25/2/3	0 days	2	37FS-2 days
39	Drain Laying	NA	As Possible	10 days	Sun 25/2/2	Tue 25/2/11	Sun 25/2/2	Tue 25/2/11	Sun 25/2/2	Tue 25/2/11	0 days	2	38FS-2 days
40	Bedding and Backfilling	NA	As Possible	8 days	Mon 25/2/10	Mon 25/2/17	Mon 25/2/10	Mon 25/2/17	Mon 25/2/10	Mon 25/2/17	0 days	0	39FS-2 days
41	Manhole Construction	NA	As Possible	10 days	Sun 25/2/16	Tue 25/2/25	Sun 25/2/16	Tue 25/2/25	Sun 25/2/16	Tue 25/2/25	0 days	2	40FS-2 days
42	Reinstatement	NA	As Possible	8 days	Wed 25/2/26	Wed 25/3/5	Wed 25/2/26	Wed 25/3/5	Wed 25/2/26	Wed 25/3/5	0 days	0	41
43	TTA Removal	NA	As Possible	2 days	Thu 25/3/6	Fri 25/3/7	Thu 25/3/6	Fri 25/3/7	Thu 25/3/6	Fri 25/3/7	0 days	0	42
44	**Stage 2**	**NA**	**As Possible**	**39 days**	**Sat 25/3/8**	**Tue 25/4/15**	**Sat 25/3/8**	**Tue 25/4/15**	**Sat 25/3/8**	**Tue 25/4/15**	**0 days**		
45	TTA Implementation	NA	As Possible	2 days	Sat 25/3/8	Sun 25/3/9	Sat 25/3/8	Sun 25/3/9	Sat 25/3/8	Sun 25/3/9	0 days	0	43
46	Breaking Ground	NA	As Possible	8 days	Sat 25/3/8	Sat 25/3/15	Sat 25/3/8	Sat 25/3/15	Sat 25/3/8	Sat 25/3/15	0 days	2	45FS-2 days
47	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/3/14	Sun 25/3/23	Fri 25/3/14	Sun 25/3/23	Fri 25/3/14	Sun 25/3/23	0 days	2	46FS-2 days
48	Drain Laying	NA	As Possible	8 days	Sat 25/3/22	Sat 25/3/29	Sat 25/3/22	Sat 25/3/29	Sat 25/3/22	Sat 25/3/29	0 days	2	47FS-2 days
49	Bedding and Backfilling	NA	As Possible	6 days	Fri 25/3/28	Wed 25/4/2	Fri 25/3/28	Wed 25/4/2	Fri 25/3/28	Wed 25/4/2	0 days	0	48FS-2 days
50	Manhole Construction	NA	As Possible	8 days	Tue 25/4/1	Tue 25/4/8	Tue 25/4/1	Tue 25/4/8	Tue 25/4/1	Tue 25/4/8	0 days	2	49FS-2 days
51	Reinstatement	NA	As Possible	6 days	Wed 25/4/9	Mon 25/4/14	Wed 25/4/9	Mon 25/4/14	Wed 25/4/9	Mon 25/4/14	0 days	0	50
52	TTA Removal	NA	As Possible	1 day	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	0 days	0	51
53	**LFT.D5~NKT Channel,1650PC,B,L=14.5,D=3.54**	**NA**	**As Possible**	**52 days**	**Wed 25/4/16**	**Fri 25/6/6**	**Wed 25/4/16**	**Fri 25/6/6**	**Wed 25/4/16**	**Fri 25/6/6**	**0 days**		
54	TTA Implementation (trial run)	NA	As Possible	4 days	Wed 25/4/16	Sat 25/4/19	Wed 25/4/16	Sat 25/4/19	Wed 25/4/16	Sat 25/4/19	0 days	0	52
55	Breaking Ground	NA	As Possible	10 days	Fri 25/4/18	Sun 25/4/27	Fri 25/4/18	Sun 25/4/27	Fri 25/4/18	Sun 25/4/27	0 days	0	54FS-2 days
56	Excavation and Lateral Support	NA	As Possible	13 days	Sat 25/4/26	Thu 25/5/8	Sat 25/4/26	Thu 25/5/8	Sat 25/4/26	Thu 25/5/8	0 days	1	55FS-2 days
57	Drain Laying	NA	As Possible	10 days	Wed 25/5/7	Fri 25/5/16	Wed 25/5/7	Fri 25/5/16	Wed 25/5/7	Fri 25/5/16	0 days	0	56FS-2 days
58	Bedding and Backfilling	NA	As Possible	8 days	Thu 25/5/15	Thu 25/5/22	Thu 25/5/15	Thu 25/5/22	Thu 25/5/15	Thu 25/5/22	0 days	0	57FS-2 days
59	Manhole Construction	NA	As Possible	10 days	Wed 25/5/21	Fri 25/5/30	Wed 25/5/21	Fri 25/5/30	Wed 25/5/21	Fri 25/5/30	0 days	0	58FS-2 days
60	Reinstatement	NA	As Possible	6 days	Sat 25/5/31	Thu 25/6/5	Sat 25/5/31	Thu 25/6/5	Sat 25/5/31	Thu 25/6/5	0 days	0	59
61	TTA Removal	NA	As Possible	1 day	Fri 25/6/6	Fri 25/6/6	Fri 25/6/6	Fri 25/6/6	Fri 25/6/6	Fri 25/6/6	0 days	0	60
62	Proposed flap valve	Thu 26/4/23	Later Than	21 days	Sat 25/6/7	Fri 25/6/27	Sat 25/6/7	Fri 25/6/27	Fri 26/4/3	Thu 26/4/23	300 days	0	61
63	**LFT.D3~LFT.D3a,1650PC,B,L=13.9,D=3.418**	**NA**	**As Possible**	**35 days**	**Sat 25/6/7**	**Fri 25/7/11**	**Sat 25/6/7**	**Fri 25/7/11**	**Sat 25/6/7**	**Fri 25/7/11**	**0 days**		
64	TTA Implementation	NA	As Possible	2 days	Sat 25/6/7	Sun 25/6/8	Sat 25/6/7	Sun 25/6/8	Sat 25/6/7	Sun 25/6/8	0 days	0	61

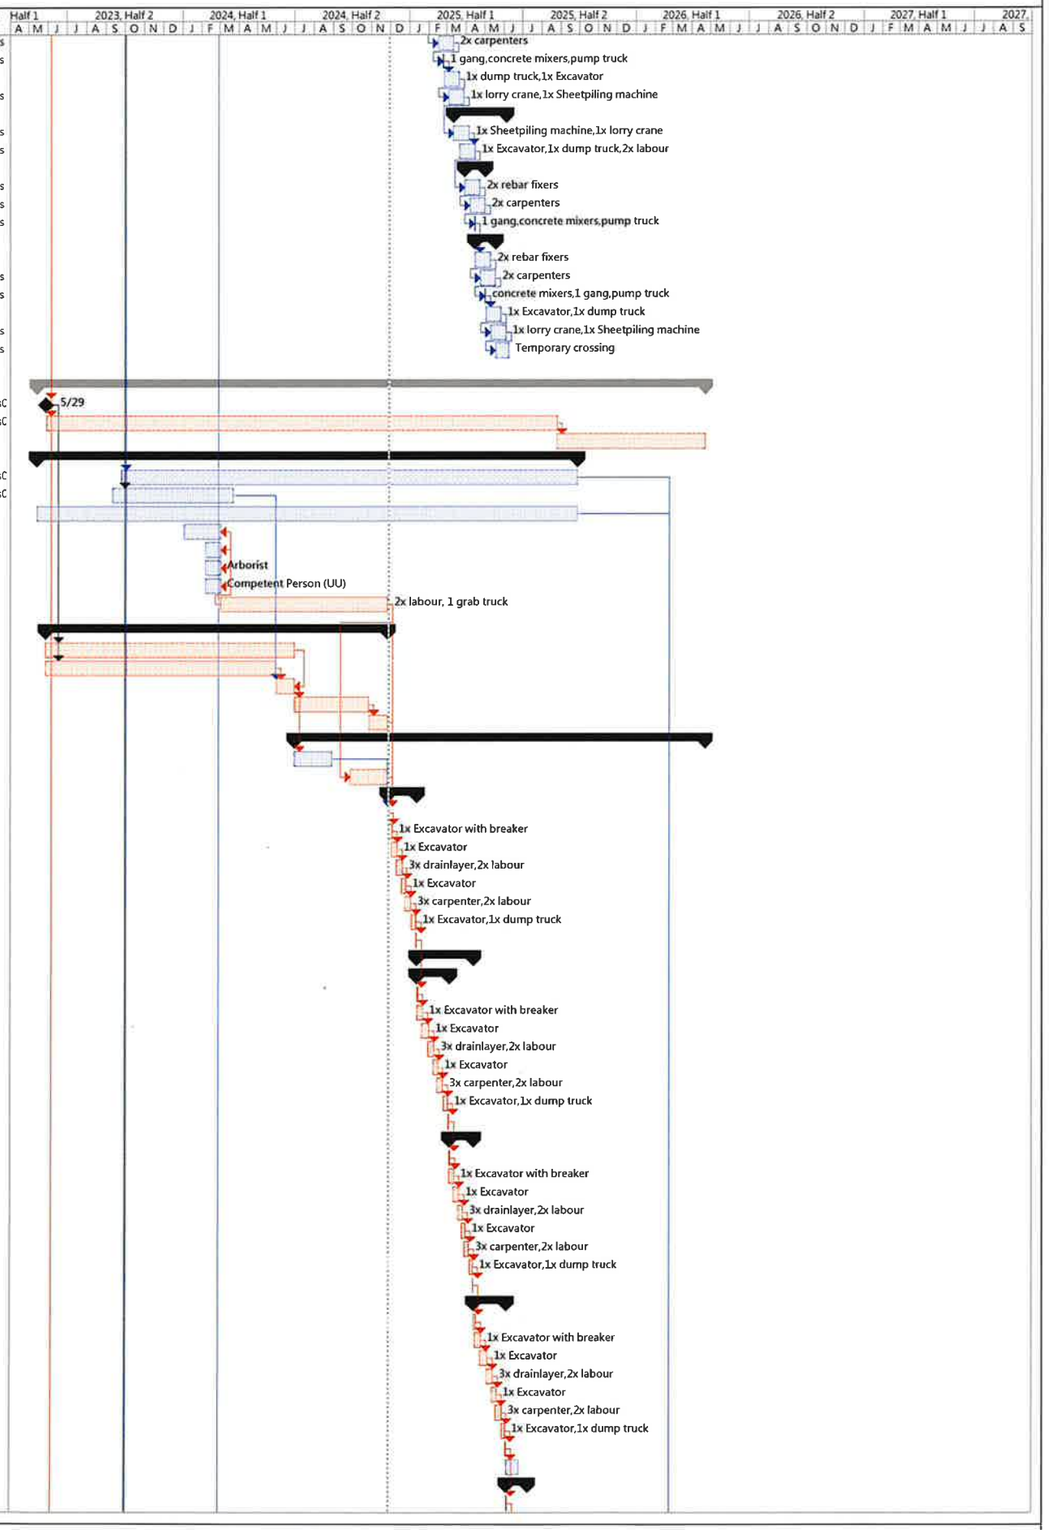


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
65	Breaking Ground	NA	As Possible	7 days	Sat 25/6/7	Fri 25/6/13	Sat 25/6/7	Fri 25/6/13	Sat 25/6/7	Fri 25/6/13	0 days	0	64FS-2 days
66	Excavation and Lateral Support	NA	As Possible	9 days	Thu 25/6/12	Fri 25/6/20	Thu 25/6/12	Fri 25/6/20	Thu 25/6/12	Fri 25/6/20	0 days	1	65FS-2 days
67	Drain Laying	NA	As Possible	7 days	Thu 25/6/19	Wed 25/6/25	Thu 25/6/19	Wed 25/6/25	Thu 25/6/19	Wed 25/6/25	0 days	0	66FS-2 days
68	Bedding and Backfilling	NA	As Possible	6 days	Tue 25/6/24	Sun 25/6/29	Tue 25/6/24	Sun 25/6/29	Tue 25/6/24	Sun 25/6/29	0 days	0	67FS-2 days
69	Manhole Construction	NA	As Possible	7 days	Sat 25/6/28	Fri 25/7/4	Sat 25/6/28	Fri 25/7/4	Sat 25/6/28	Fri 25/7/4	0 days	0	68FS-2 days
70	Reinstatement	NA	As Possible	6 days	Sat 25/7/5	Thu 25/7/10	Sat 25/7/5	Thu 25/7/10	Sat 25/7/5	Thu 25/7/10	0 days	0	69
71	TTA Removal	NA	As Possible	1 day	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	0 days	0	70
72	**LFT.D2~LFT.D3,1650PC,B,L=39,D=3.34**	**NA**	**As Possible**	**82 days**	**Sat 25/7/12**	**Wed 25/10/1**	**Sat 25/7/12**	**Wed 25/10/1**	**Sat 25/7/12**	**Wed 25/10/1**	**0 days**		
73	**Stage 1**	**NA**	**As Possible**	**46 days**	**Sat 25/7/12**	**Tue 25/8/26**	**Sat 25/7/12**	**Tue 25/8/26**	**Sat 25/7/12**	**Tue 25/8/26**	**0 days**		
74	TTA Implementation	NA	As Possible	2 days	Sat 25/7/12	Sun 25/7/13	Sat 25/7/12	Sun 25/7/13	Sat 25/7/12	Sun 25/7/13	0 days	0	71
75	Breaking Ground	NA	As Possible	9 days	Sat 25/7/12	Sun 25/7/20	Sat 25/7/12	Sun 25/7/20	Sat 25/7/12	Sun 25/7/20	0 days	2	74FS-2 days
76	Excavation and Lateral Support	NA	As Possible	11 days	Sat 25/7/19	Tue 25/7/29	Sat 25/7/19	Tue 25/7/29	Sat 25/7/19	Tue 25/7/29	0 days	2	75FS-2 days
77	Drain Laying	NA	As Possible	9 days	Mon 25/7/28	Tue 25/8/5	Mon 25/7/28	Tue 25/8/5	Mon 25/7/28	Tue 25/8/5	0 days	2	76FS-2 days
78	Bedding and Backfilling	NA	As Possible	7 days	Mon 25/8/4	Sun 25/8/10	Mon 25/8/4	Sun 25/8/10	Mon 25/8/4	Sun 25/8/10	0 days	0	77FS-2 days
79	Manhole Construction	NA	As Possible	9 days	Sat 25/8/9	Sun 25/8/17	Sat 25/8/9	Sun 25/8/17	Sat 25/8/9	Sun 25/8/17	0 days	2	78FS-2 days
80	Reinstatement	NA	As Possible	7 days	Mon 25/8/18	Sun 25/8/24	Mon 25/8/18	Sun 25/8/24	Mon 25/8/18	Sun 25/8/24	0 days	0	79
81	TTA Removal	NA	As Possible	2 days	Mon 25/8/25	Tue 25/8/26	Mon 25/8/25	Tue 25/8/26	Mon 25/8/25	Tue 25/8/26	0 days	0	80
82	**Stage 2**	**NA**	**As Possible**	**36 days**	**Wed 25/8/27**	**Wed 25/10/1**	**Wed 25/8/27**	**Wed 25/10/1**	**Wed 25/8/27**	**Wed 25/10/1**	**0 days**		
83	TTA Implementation	NA	As Possible	2 days	Wed 25/8/27	Thu 25/8/28	Wed 25/8/27	Thu 25/8/28	Wed 25/8/27	Thu 25/8/28	0 days	0	81
84	Breaking Ground	NA	As Possible	7 days	Wed 25/8/27	Tue 25/9/2	Wed 25/8/27	Tue 25/9/2	Wed 25/8/27	Tue 25/9/2	0 days	0	83FS-2 days
85	Excavation and Lateral Support	NA	As Possible	9 days	Mon 25/9/1	Tue 25/9/9	Mon 25/9/1	Tue 25/9/9	Mon 25/9/1	Tue 25/9/9	0 days	1	84FS-2 days
86	Drain Laying	NA	As Possible	7 days	Mon 25/9/8	Sun 25/9/14	Mon 25/9/8	Sun 25/9/14	Mon 25/9/8	Sun 25/9/14	0 days	1	85FS-2 days
87	Bedding and Backfilling	NA	As Possible	6 days	Sat 25/9/13	Thu 25/9/18	Sat 25/9/13	Thu 25/9/18	Sat 25/9/13	Thu 25/9/18	0 days	0	86FS-2 days
88	Manhole Construction	NA	As Possible	8 days	Wed 25/9/17	Wed 25/9/24	Wed 25/9/17	Wed 25/9/24	Wed 25/9/17	Wed 25/9/24	0 days	1	87FS-2 days
89	Reinstatement	NA	As Possible	6 days	Thu 25/9/25	Tue 25/9/30	Thu 25/9/25	Tue 25/9/30	Thu 25/9/25	Tue 25/9/30	0 days	0	88
90	TTA Removal	NA	As Possible	1 day	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	0 days	0	89
91	**LFT.D1b~LFT.D2,1650PC,B,L=45.56,D=3.34**	**NA**	**As Possible**	**101 days**	**Thu 25/10/2**	**Sat 26/1/10**	**Thu 25/10/2**	**Sat 26/1/10**	**Thu 25/10/2**	**Sat 26/1/10**	**0 days**		
92	**Stage 1**	**NA**	**As Possible**	**51 days**	**Thu 25/10/2**	**Fri 25/11/21**	**Thu 25/10/2**	**Fri 25/11/21**	**Thu 25/10/2**	**Fri 25/11/21**	**0 days**		
93	TTA Implementation	NA	As Possible	2 days	Thu 25/10/2	Fri 25/10/3	Thu 25/10/2	Fri 25/10/3	Thu 25/10/2	Fri 25/10/3	0 days	0	90
94	Breaking Ground	NA	As Possible	10 days	Thu 25/10/2	Sat 25/10/11	Thu 25/10/2	Sat 25/10/11	Thu 25/10/2	Sat 25/10/11	0 days	2	93FS-2 days
95	Excavation and Lateral Support	NA	As Possible	11 days	Fri 25/10/10	Mon 25/10/20	Fri 25/10/10	Mon 25/10/20	Fri 25/10/10	Mon 25/10/20	0 days	2	94FS-2 days
96	Drain Laying	NA	As Possible	10 days	Sun 25/10/19	Tue 25/10/28	Sun 25/10/19	Tue 25/10/28	Sun 25/10/19	Tue 25/10/28	0 days	2	95FS-2 days
97	Bedding and Backfilling	NA	As Possible	8 days	Mon 25/10/27	Mon 25/11/3	Mon 25/10/27	Mon 25/11/3	Mon 25/10/27	Mon 25/11/3	0 days	0	96FS-2 days
98	Manhole Construction	NA	As Possible	10 days	Sun 25/11/2	Tue 25/11/11	Sun 25/11/2	Tue 25/11/11	Sun 25/11/2	Tue 25/11/11	0 days	2	97FS-2 days
99	Reinstatement	NA	As Possible	8 days	Wed 25/11/12	Wed 25/11/19	Wed 25/11/12	Wed 25/11/19	Wed 25/11/12	Wed 25/11/19	0 days	0	98
100	TTA Removal	NA	As Possible	2 days	Thu 25/11/20	Fri 25/11/21	Thu 25/11/20	Fri 25/11/21	Thu 25/11/20	Fri 25/11/21	0 days	0	99
101	**Stage 2**	**NA**	**As Possible**	**50 days**	**Sat 25/11/22**	**Sat 26/1/10**	**Sat 25/11/22**	**Sat 26/1/10**	**Sat 25/11/22**	**Sat 26/1/10**	**0 days**		
102	TTA Implementation	NA	As Possible	2 days	Sat 25/11/22	Sun 25/11/23	Sat 25/11/22	Sun 25/11/23	Sat 25/11/22	Sun 25/11/23	0 days	0	100
103	Breaking Ground	NA	As Possible	10 days	Sat 25/11/22	Mon 25/12/1	Sat 25/11/22	Mon 25/12/1	Sat 25/11/22	Mon 25/12/1	0 days	2	102FS-2 days
104	Excavation and Lateral Support	NA	As Possible	11 days	Sun 25/11/30	Wed 25/12/10	Sun 25/11/30	Wed 25/12/10	Sun 25/11/30	Wed 25/12/10	0 days	2	103FS-2 days
105	Drain Laying	NA	As Possible	10 days	Tue 25/12/9	Thu 25/12/18	Tue 25/12/9	Thu 25/12/18	Tue 25/12/9	Thu 25/12/18	0 days	2	104FS-2 days
106	Bedding and Backfilling	NA	As Possible	8 days	Wed 25/12/17	Wed 25/12/24	Wed 25/12/17	Wed 25/12/24	Wed 25/12/17	Wed 25/12/24	0 days	0	105FS-2 days
107	Manhole Construction	NA	As Possible	10 days	Tue 25/12/23	Thu 26/1/1	Tue 25/12/23	Thu 26/1/1	Tue 25/12/23	Thu 26/1/1	0 days	2	106FS-2 days
108	Reinstatement	NA	As Possible	8 days	Fri 26/1/2	Fri 26/1/9	Fri 26/1/2	Fri 26/1/9	Fri 26/1/2	Fri 26/1/9	0 days	0	107
109	TTA Removal	NA	As Possible	1 day	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	0 days	0	108
110	**LFT.D1a~LFT.D1b,1650PC,B,L=25.59,D=3.411**	**NA**	**As Possible**	**46 days**	**Sun 26/1/11**	**Wed 26/2/25**	**Sun 26/1/11**	**Wed 26/2/25**	**Sun 26/1/11**	**Wed 26/2/25**	**0 days**		
111	TTA Implementation	NA	As Possible	2 days	Sun 26/1/11	Mon 26/1/12	Sun 26/1/11	Mon 26/1/12	Sun 26/1/11	Mon 26/1/12	0 days	0	109
112	Breaking Ground	NA	As Possible	9 days	Sun 26/1/11	Mon 26/1/19	Sun 26/1/11	Mon 26/1/19	Sun 26/1/11	Mon 26/1/19	0 days	0	111FS-2 days
113	Excavation and Lateral Support	NA	As Possible	10 days	Sun 26/1/18	Tue 26/1/27	Sun 26/1/18	Tue 26/1/27	Sun 26/1/18	Tue 26/1/27	0 days	2	112FS-2 days
114	Drain Laying	NA	As Possible	8 days	Mon 26/1/26	Mon 26/2/2	Mon 26/1/26	Mon 26/2/2	Mon 26/1/26	Mon 26/2/2	0 days	2	113FS-2 days
115	Bedding and Backfilling	NA	As Possible	8 days	Sun 26/2/1	Sun 26/2/8	Sun 26/2/1	Sun 26/2/8	Sun 26/2/1	Sun 26/2/8	0 days	1	114FS-2 days
116	Manhole Construction	NA	As Possible	10 days	Sat 26/2/7	Mon 26/2/16	Sat 26/2/7	Mon 26/2/16	Sat 26/2/7	Mon 26/2/16	0 days	2	115FS-2 days
117	Reinstatement	NA	As Possible	8 days	Tue 26/2/17	Tue 26/2/24	Tue 26/2/17	Tue 26/2/24	Tue 26/2/17	Tue 26/2/24	0 days	1	116
118	TTA Removal	NA	As Possible	1 day	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	0 days	0	117
119	**LFT.D1~LFT.D1a,1650PC,B,L=5.65,D=3.411**	**NA**	**As Possible**	**29 days**	**Thu 26/2/26**	**Thu 26/3/26**	**Thu 26/2/26**	**Thu 26/3/26**	**Thu 26/2/26**	**Thu 26/3/26**	**0 days**		
120	TTA Implementation	NA	As Possible	2 days	Thu 26/2/26	Fri 26/2/27	Thu 26/2/26	Fri 26/2/27	Thu 26/2/26	Fri 26/2/27	0 days	0	118,6,8
121	Breaking Ground	NA	As Possible	7 days	Thu 26/2/26	Wed 26/3/4	Thu 26/2/26	Wed 26/3/4	Thu 26/2/26	Wed 26/3/4	0 days	0	120FS-2 days
122	Excavation and Lateral Support	NA	As Possible	7 days	Tue 26/3/3	Mon 26/3/9	Tue 26/3/3	Mon 26/3/9	Tue 26/3/3	Mon 26/3/9	0 days	1	121FS-2 days
123	Drain Laying	NA	As Possible	7 days	Sun 26/3/8	Sat 26/3/14	Sun 26/3/8	Sat 26/3/14	Sun 26/3/8	Sat 26/3/14	0 days	1	122FS-2 days
124	Bedding and Backfilling	NA	As Possible	4 days	Fri 26/3/13	Mon 26/3/16	Fri 26/3/13	Mon 26/3/16	Fri 26/3/13	Mon 26/3/16	0 days	0	123FS-2 days
125	Manhole Construction	NA	As Possible	7 days	Sun 26/3/15	Sat 26/3/21	Sun 26/3/15	Sat 26/3/21	Sun 26/3/15	Sat 26/3/21	0 days	0	124FS-2 days
126	Reinstatement	NA	As Possible	4 days	Sun 26/3/22	Wed 26/3/25	Sun 26/3/22	Wed 26/3/25	Sun 26/3/22	Wed 26/3/25	0 days	0	125
127	TTA Removal	NA	As Possible	1 day	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	0 days	0	126
128	CCTV inspection and T&C	NA	As Possible	14 days	Fri 26/3/27	Thu 26/4/9	Fri 26/3/27	Thu 26/4/9	Fri 26/3/27	Thu 26/4/9	0 days	4	127
129	Final Reinstatement	Thu 26/4/23	Later Than	14 days	Fri 26/4/10	Thu 26/4/23	Fri 26/4/10	Thu 26/4/23	Fri 26/4/10	Thu 26/4/23	0 days	4	128
112													
113	**Section IV**	**NA**	**As Possible**	**1225 days**	**Tue 23/5/30**	**Mon 26/10/5**	**Tue 23/5/30**	**Mon 26/10/5**	**Tue 23/5/30**	**Fri 27/4/2**	**0 days**		
2	access date of Portion D	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	Thu 25/11/27	Wed 26/6/24	912 days	0	\\WingTatNasC
3	section IV (Ha Che)	Thu 26/5/28	Later Than	1095 days	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	Tue 23/5/30	Thu 26/5/28	0 days	0	\\WingTatNasC
4	Planned Completion Day	########	Later Than	130 days	Fri 26/5/29	Mon 26/10/5	Fri 26/5/29	Mon 26/10/5	Fri 26/5/29	Mon 26/10/5	0 days	0	3
5	Early access (portion)	NA	As Possible	144 days	Tue 23/5/30	Fri 23/10/20	Tue 23/5/30	Fri 23/10/20	Fri 23/7/14	Mon 23/12/4	45 days	0	\\WingTatNasC
6	Access to remaining STLA	NA	As Possible	1 day	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	Wed 26/6/24	Wed 26/6/24	912 days	0	2FS-1 day
7	Private Land Leasing	NA	As Possible	12 days	Sat 23/10/21	Wed 23/11/1	Sat 23/10/21	Wed 23/11/1	Tue 23/12/12	Sat 23/12/23	52 days	0	5
8	**Site Establishment**	**NA**	**As Possible**	**869 days**	**Tue 23/9/12**	**Tue 26/1/27**	**Tue 23/9/12**	**Tue 26/1/27**	**##########**	**Mon 26/10/5**	**48 days**		
9	Prepare and Accept Temp. Works Design and Method Statement	NA	As Possible	855 days	Tue 23/9/26	Tue 26/1/27	Tue 23/9/26	Tue 26/1/27	Sun 23/12/10	Sun 26/4/12	75 days	0	\\WingTatNasC
10	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	35 days	Tue 23/9/12	Mon 23/10/16	Tue 23/9/12	Mon 23/10/16	Mon 23/10/30	Sun 23/12/3	48 days	0	\\WingTatNasC
11	Initial Survey [A]	NA	As Possible	831 days	Fri 23/10/20	Tue 26/1/27	Fri 23/10/20	Tue 26/1/27	Wed 24/1/3	Sun 26/4/12	75 days	0	10,5FS-1 day
13	Initial Safety & Environmental measures [A]	NA	As Possible	20 days	Fri 23/10/20	Wed 23/11/8	Fri 23/10/20	Wed 23/11/8	Mon 23/12/4	Sat 23/12/23	45 days	0	10,5FS-1 day
15	EIAO Commencement of Construction [A]	NA	As Possible	1 day	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Thu 24/3/7	Thu 24/3/7	15 days	0	\\WingTatNasC
17	Environmental Baseline Monitoring [A]	########	Later Than	29 days	Tue 24/1/23	Tue 24/2/20	Tue 24/1/23	Tue 24/2/20	Mon 26/9/7	Mon 26/10/5	958 days	0	15FS-30 days
18	Freshwater Crab Translocation Plan [A]	########	Later Than	30 days	Sat 23/12/23	Mon 24/1/22	Sat 23/12/23	Mon 24/1/22	Sun 26/9/6	Mon 26/10/5	988 days	0	7,15SF-30 days
19	Condition Survey & Str. Assessment (Shui Kan Shek, Fu Hing Garden, Twin 150	NA	As Possible	365 days	Thu 23/11/9	Thu 24/11/7	Thu 23/11/9	Thu 24/11/7	Thu 25/8/7	Thu 26/8/6	637 days	0	7,13

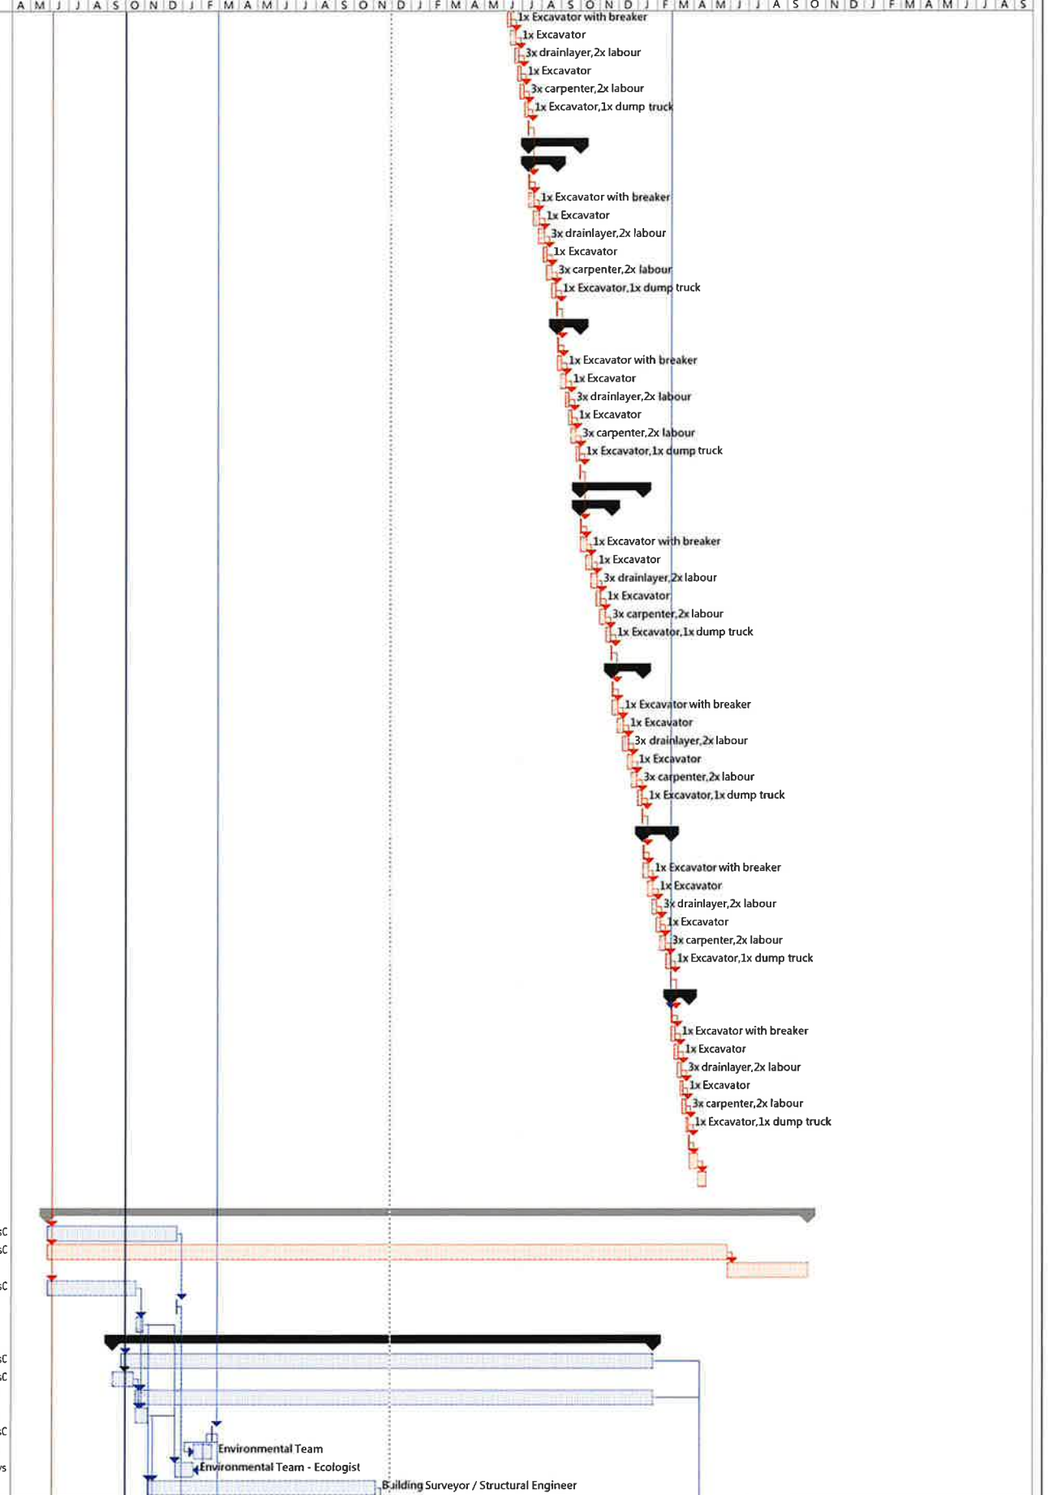


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
20	UU detection [A]	NA	As Possible	20 days	Thu 23/11/9	Tue 23/11/28	Thu 23/11/9	Tue 23/11/28	Sat 24/1/13	Thu 24/2/1	65 days	0	7,13
21	Vegetation Survey [A]	NA	As Possible	20 days	Thu 23/11/9	Tue 23/11/28	Thu 23/11/9	Tue 23/11/28	Sat 24/1/13	Thu 24/2/1	65 days	0	7,13
22	Tree Survey and Felling [A]	NA	As Possible	20 days	Thu 23/11/9	Tue 23/11/28	Thu 23/11/9	Tue 23/11/28	Sun 23/12/24	Fri 24/1/12	45 days	0	7,13
23	Setup of instrumentation and monitoring [A]	NA	As Possible	20 days	Wed 23/11/29	Mon 23/12/18	Wed 23/11/29	Mon 23/12/18	Sat 24/1/13	Thu 24/2/1	45 days	0	22
24	Site Clearance [A]	NA	As Possible	21 days	Tue 23/12/19	Mon 24/1/8	Tue 23/12/19	Mon 24/1/8	Fri 24/2/2	Thu 24/2/22	45 days	0	23,21
25	Establish access(es) to channels [A]	NA	As Possible	21 days	Tue 23/12/19	Mon 24/1/8	Tue 23/12/19	Mon 24/1/8	Fri 24/2/2	Thu 24/2/22	45 days	0	20,23
26	Guarding / Barrier / Hoarding [A]	NA	As Possible	21 days	Tue 23/12/19	Mon 24/1/8	Tue 23/12/19	Mon 24/1/8	Fri 24/2/2	Thu 24/2/22	45 days	0	20,23
27	**Drainage Channel Works (East)**	**NA**	**As Possible**	**1083 days**	**Thu 23/10/19**	**Mon 26/10/5**	**Thu 23/10/19**	**Mon 26/10/5**	**Fri 24/2/23**	**Fri 27/4/2**	**127 days**		
28	HC05 CH.A284.946~CH.A339.556 (Ex. CH Str. Assessment)	########	Later Than	60 days	Fri 24/11/8	Mon 25/1/6	Fri 24/11/8	Mon 25/1/6	Fri 26/8/7	Mon 26/10/5	637 days	0	19
29	(Deleted in PMI) Demolish & relocate wall, gate YLL797/2	NA	As Possible	30 days	Tue 23/12/26	Wed 24/1/24	Tue 23/12/26	Wed 24/1/24	Thu 26/6/25	Fri 26/7/24	912 days	0	6
30	(Deleted in PMI) HC01 CH.A11.13~CH.A18.14	NA	As Possible	45 days	Thu 24/1/25	Sat 24/3/9	Thu 24/1/25	Sat 24/3/9	Sat 26/7/25	Mon 26/9/7	912 days	5	29
31	(Deleted in PMI) Pedestrian & Vehicular Crossing no. 1 (Box Culvert no. 1)	########	Later Than	28 days	Sun 24/3/10	Sat 24/4/6	Sun 24/3/10	Sat 24/4/6	Tue 26/9/8	Mon 26/10/5	912 days	0	30
32	Pedestrian & Vehicular Crossing no. 2 (Box Culvert no. 2) [A]	########	Later Than	28 days	Thu 24/2/8	Wed 24/3/6	Thu 24/2/8	Wed 24/3/6	Fri 24/2/23	Thu 24/3/21	15 days	0	26,25,15FS-14 d
33	**HC02 CH.A18.14~CH.A120.261 (BC1~2)**	**NA**	**As Possible**	**359 days**	**Thu 23/10/19**	**Fri 24/10/11**	**Thu 23/10/19**	**Fri 24/10/11**	**Fri 24/3/22**	**Fri 27/4/2**	**155 days**		
34	EWN/007 NCE/001 Ambiguity on Drawings	########	Earlier Than	30 days	Thu 23/10/19	Fri 23/11/17	Thu 23/10/19	Fri 23/11/17	Fri 27/2/12	Sat 27/3/13	1212 days	0	
35	C9 tender for Precast units [A]	NA	As Possible	20 days	Sat 23/11/18	Thu 23/12/7	Sat 23/11/18	Thu 23/12/7	Sun 27/3/14	Fri 27/4/2	1212 days	0	34
36	Sheetpiling & Temp. Drainage Diversion [A]	NA	As Possible	44 days	Thu 24/3/7	Fri 24/4/19	Thu 24/3/7	Fri 24/4/19	Fri 24/3/22	Sat 24/5/4	15 days	1	32
37	Excavation and Lateral Support [A]	NA	As Possible	44 days	Tue 24/4/2	Wed 24/5/15	Tue 24/4/2	Wed 24/5/15	Wed 24/4/17	Thu 24/5/30	15 days	1	36FS-18 days
38	**Walls**	**NA**	**As Possible**	**68 days**	**Sun 24/4/28**	**Thu 24/7/4**	**Sun 24/4/28**	**Thu 24/7/4**	**Mon 24/5/13**	**Fri 24/7/19**	**15 days**		
39	Install precast portion (double beam) [A]	NA	As Possible	68 days	Sun 24/4/28	Thu 24/7/4	Sun 24/4/28	Thu 24/7/4	Mon 24/5/13	Fri 24/7/19	15 days	0	37FS-18 days
40	**Ground Beams**	**NA**	**As Possible**	**40 days**	**Mon 24/6/10**	**Fri 24/7/19**	**Mon 24/6/10**	**Fri 24/7/19**	**Tue 24/6/25**	**Sat 24/8/3**	**15 days**		
41	Rebar Fixing [A]	NA	As Possible	30 days	Mon 24/6/10	Tue 24/7/9	Mon 24/6/10	Tue 24/7/9	Tue 24/6/25	Wed 24/7/24	15 days	1	39FS-25 days
42	Formwork Erection and Cast-in items [A]	NA	As Possible	30 days	Thu 24/6/20	Fri 24/7/19	Thu 24/6/20	Fri 24/7/19	Fri 24/7/5	Sat 24/8/3	15 days	1	41FS-20 days
43	Concreting [A]	NA	As Possible	14 days	Sun 24/6/30	Sat 24/7/13	Sun 24/6/30	Sat 24/7/13	Mon 24/7/15	Sun 24/7/28	15 days	0	42FS-20 days
44	**Top Wall**	**NA**	**As Possible**	**50 days**	**Sun 24/7/14**	**Sun 24/9/1**	**Sun 24/7/14**	**Sun 24/9/1**	**Mon 24/7/29**	**Mon 24/9/16**	**15 days**		
45	Rebar Fixing [A]	NA	As Possible	35 days	Sun 24/7/14	Sat 24/8/17	Sun 24/7/14	Sat 24/8/17	Mon 24/7/29	Sun 24/9/1	15 days	1	43
46	Formwork Erection and Cast-in items [A]	NA	As Possible	35 days	Mon 24/7/29	Sun 24/9/1	Mon 24/7/29	Sun 24/9/1	Tue 24/8/13	Mon 24/9/16	15 days	1	45FS-20 days
47	Concreting [A]	NA	As Possible	14 days	Tue 24/8/13	Mon 24/8/26	Tue 24/8/13	Mon 24/8/26	Tue 24/9/3	Mon 24/9/16	21 days	0	46FS-20 days
48	Backfilling and Compaction	NA	As Possible	30 days	Tue 24/8/27	Wed 24/9/25	Tue 24/8/27	Wed 24/9/25	Fri 26/8/7	Sat 26/9/5	710 days	0	47
49	Removal of Sheetpiles	NA	As Possible	30 days	Thu 24/9/12	Fri 24/10/11	Thu 24/9/12	Fri 24/10/11	Sun 26/8/23	Mon 26/9/21	710 days	0	48FS-14 days
50	Animal Escape Ramp [A]	########	Later Than	28 days	Sat 24/9/28	Fri 24/10/25	Sat 24/9/28	Fri 24/10/25	Tue 26/9/8	Mon 26/10/5	710 days	0	49FS-14 days
51	Demolish & relocate toilet YLL797/5 [A]	NA	As Possible	20 days	Mon 24/8/19	Sat 24/9/7	Mon 24/8/19	Sat 24/9/7	Tue 24/9/3	Sun 24/9/22	15 days	0	44FS-14 days
52	Demolish & relocate container YLL797/6 [A]	NA	As Possible	20 days	Mon 24/8/19	Sat 24/9/7	Mon 24/8/19	Sat 24/9/7	Tue 24/9/3	Sun 24/9/22	15 days	0	44FS-14 days
53	Demolish & relocate porch YLL797/7 [A]	NA	As Possible	20 days	Mon 24/8/19	Sat 24/9/7	Mon 24/8/19	Sat 24/9/7	Tue 24/9/3	Sun 24/9/22	15 days	0	44FS-14 days
54	Demolish & relocate fencing, retaining wall YLL797/10,11 [A]	NA	As Possible	20 days	Mon 24/8/19	Sat 24/9/7	Mon 24/8/19	Sat 24/9/7	Tue 24/9/3	Sun 24/9/22	15 days	0	44FS-14 days
55	**HC03 CH.A126.235~CH.A187.706 (BC2~3)**	**NA**	**As Possible**	**311 days**	**Wed 24/8/14**	**Fri 25/6/20**	**Wed 24/8/14**	**Fri 25/6/20**	**Wed 24/8/14**	**Fri 25/6/20**	**0 days**		
56	[PMI-037] Removal of existing structural features protruding into Work Sit	########	Earlier Than	25 days	Wed 24/8/14	Sat 24/9/7	Wed 24/8/14	Sat 24/9/7	Wed 24/8/14	Sat 24/9/7	0 days	0	
57	[PMI-040] Updated Channel Width of Drainage Channel between Chainage CH.A163 to CH.A209 at Ha Che (impact to be ascertained)	Wed 24/8/28	Start No Earlier Than	30 days	Wed 24/8/28	Thu 24/9/26	Wed 24/8/28	Thu 24/9/26	Wed 24/8/28	Thu 24/9/26	0 days	0	
58	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	50 days	Sun 24/9/8	Sun 24/10/27	Sun 24/9/8	Sun 24/10/27	Sun 24/9/8	Sun 24/10/27	0 days	2	51FS-15 days,5
59	Excavation and Lateral Support	NA	As Possible	50 days	Mon 24/10/14	Mon 24/12/2	Mon 24/10/14	Mon 24/12/2	Mon 24/10/14	Mon 24/12/2	0 days	2	58FS-14 days
60	**Ground Beams**	**NA**	**As Possible**	**85 days**	**Tue 24/11/19**	**Tue 25/2/11**	**Tue 24/11/19**	**Tue 25/2/11**	**Tue 24/11/19**	**Tue 25/2/11**	**0 days**		
61	Rebar Fixing	NA	As Possible	50 days	Tue 24/11/19	Tue 25/1/7	Tue 24/11/19	Tue 25/1/7	Tue 24/11/19	Tue 25/1/7	0 days	2	59FS-14 days
62	Formwork Erection and Cast-in items	NA	As Possible	50 days	Tue 24/12/24	Tue 25/2/11	Tue 24/12/24	Tue 25/2/11	Tue 24/12/24	Tue 25/2/11	0 days	2	61FS-15 days
63	Concreting	NA	As Possible	14 days	Tue 25/1/28	Mon 25/2/10	Tue 25/1/28	Mon 25/2/10	Tue 25/1/28	Mon 25/2/10	0 days	0	62FS-15 days
64	**Wall**	**NA**	**As Possible**	**85 days**	**Tue 25/2/11**	**Tue 25/5/6**	**Tue 25/2/11**	**Tue 25/5/6**	**Tue 25/2/11**	**Tue 25/5/6**	**0 days**		
65	Rebar Fixing	NA	As Possible	50 days	Tue 25/2/11	Tue 25/4/1	Tue 25/2/11	Tue 25/4/1	Tue 25/2/11	Tue 25/4/1	0 days	2	63
66	Formwork Erection and Cast-in items	NA	As Possible	50 days	Tue 25/3/18	Tue 25/5/6	Tue 25/3/18	Tue 25/5/6	Tue 25/3/18	Tue 25/5/6	0 days	2	65FS-15 days
67	Concreting	NA	As Possible	14 days	Tue 25/4/22	Mon 25/5/5	Tue 25/4/22	Mon 25/5/5	Tue 25/4/22	Mon 25/5/5	0 days	0	66FS-15 days
68	Backfilling and Compaction	NA	As Possible	30 days	Tue 25/5/6	Wed 25/6/4	Tue 25/5/6	Wed 25/6/4	Tue 25/5/6	Wed 25/6/4	0 days	0	67
69	Removal of Sheetpiles	NA	As Possible	30 days	Thu 25/5/22	Fri 25/6/20	Thu 25/5/22	Fri 25/6/20	Thu 25/5/22	Fri 25/6/20	0 days	0	68FS-14 days
70	Pedestrian & Vehicular Crossing no. 1 (Box Culvert no. 3)	NA	As Possible	60 days	Sat 25/6/7	Tue 25/8/5	Sat 25/6/7	Tue 25/8/5	Sat 25/6/7	Tue 25/8/5	0 days	0	69FS-14 days
71	Demolish & relocate drainage channel YLL797/12	NA	As Possible	20 days	Wed 25/7/23	Mon 25/8/11	Wed 25/7/23	Mon 25/8/11	Wed 25/7/23	Mon 25/8/11	0 days	0	70FS-14 days
72	[PMI016] Revised Drainage Channel Details	Tue 24/7/23	Earlier Than	90 days	Tue 24/7/23	Sun 24/10/20	Tue 24/7/23	Sun 24/10/20	Tue 25/4/29	Sun 25/7/27	280 days		
73	**HC04 CH.A195.853~CH.A284.946 (BC3~Ex. CH)**	**NA**	**As Possible**	**198 days**	**Mon 25/7/28**	**Tue 26/2/10**	**Mon 25/7/28**	**Tue 26/2/10**	**Mon 25/7/28**	**Tue 26/2/10**	**0 days**		
74	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	40 days	Mon 25/7/28	Fri 25/9/5	Mon 25/7/28	Fri 25/9/5	Mon 25/7/28	Fri 25/9/5	0 days	2	71FS-15 days,7
75	Excavation and Lateral Support	NA	As Possible	40 days	Fri 25/8/22	Tue 25/9/30	Fri 25/8/22	Tue 25/9/30	Fri 25/8/22	Tue 25/9/30	0 days	2	74FS-15 days
76	**Ground and Edge Beams**	**NA**	**As Possible**	**60 days**	**Tue 25/9/16**	**Fri 25/11/14**	**Tue 25/9/16**	**Fri 25/11/14**	**Tue 25/9/16**	**Fri 25/11/14**	**0 days**		
77	Rebar Fixing	NA	As Possible	40 days	Tue 25/9/16	Sat 25/10/25	Tue 25/9/16	Sat 25/10/25	Tue 25/9/16	Sat 25/10/25	0 days	2	75FS-15 days
78	Formwork Erection and Cast-in items	NA	As Possible	40 days	Mon 25/10/6	Fri 25/11/14	Mon 25/10/6	Fri 25/11/14	Mon 25/10/6	Fri 25/11/14	0 days	2	77FS-20 days
79	Concreting	NA	As Possible	14 days	Sun 25/10/26	Sat 25/11/8	Sun 25/10/26	Sat 25/11/8	Sun 25/10/26	Sat 25/11/8	0 days	0	78FS-20 days
80	**Walls**	**NA**	**As Possible**	**60 days**	**Sun 25/11/9**	**Wed 26/1/7**	**Sun 25/11/9**	**Wed 26/1/7**	**Sun 25/11/9**	**Wed 26/1/7**	**0 days**		
81	Rebar Fixing	NA	As Possible	40 days	Sun 25/11/9	Thu 25/12/18	Sun 25/11/9	Thu 25/12/18	Sun 25/11/9	Thu 25/12/18	0 days	2	79
82	Formwork Erection and Cast-in items	NA	As Possible	40 days	Sat 25/11/29	Wed 26/1/7	Sat 25/11/29	Wed 26/1/7	Sat 25/11/29	Wed 26/1/7	0 days	2	81FS-20 days
83	Concreting	NA	As Possible	14 days	Fri 25/12/19	Thu 26/1/1	Fri 25/12/19	Thu 26/1/1	Fri 25/12/19	Thu 26/1/1	0 days	0	82FS-20 days
84	Backfilling and Compaction	NA	As Possible	30 days	Fri 26/1/2	Sat 26/1/31	Fri 26/1/2	Sat 26/1/31	Fri 26/1/2	Sat 26/1/31	0 days	0	83
85	Removal of Sheetpiles	NA	As Possible	30 days	Mon 26/1/12	Tue 26/2/10	Mon 26/1/12	Tue 26/2/10	Mon 26/1/12	Tue 26/2/10	0 days	0	84FS-20 days
86	2x300 pipe with flap valve	########	Later Than	30 days	Thu 26/1/22	Fri 26/2/20	Thu 26/1/22	Fri 26/2/20	Sun 26/9/6	Mon 26/10/5	227 days	4	85FS-20 days
87	C9 tender procedure for HC06-08	Fri 24/6/28	Earlier Than	90 days	Fri 24/6/28	Wed 24/9/25	Fri 24/6/28	Wed 24/9/25	Tue 24/8/27	Sun 24/11/24	60 days		
88	Demolish & relocate metal frame YLL797/28,30,33	NA	As Possible	20 days	Thu 24/9/26	Tue 24/10/15	Thu 24/9/26	Tue 24/10/15	Mon 24/11/25	Sat 24/12/14	60 days	0	87
89	Demolish & relocate storage YLL797/29	NA	As Possible	20 days	Thu 24/9/26	Tue 24/10/15	Thu 24/9/26	Tue 24/10/15	Mon 24/11/25	Sat 24/12/14	60 days	0	87
90	Demolish & relocate retaining wall YLL797/32	NA	As Possible	20 days	Thu 24/9/26	Tue 24/10/15	Thu 24/9/26	Tue 24/10/15	Mon 24/11/25	Sat 24/12/14	60 days	0	87
91	[NCExxx] Additional request from landlord by HC06,07	########	Earlier Than	75 days	Mon 24/9/16	Fri 24/11/29	Mon 24/9/16	Fri 24/11/29	Mon 24/9/16	Fri 24/11/29	0 days	0	
92	**HC06 CH.A339.556~CH.A400.00**	**NA**	**As Possible**	**187 days**	**Sat 24/11/30**	**Wed 25/6/4**	**Sat 24/11/30**	**Wed 25/6/4**	**Sat 24/11/30**	**Wed 25/6/4**	**0 days**		
93	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	35 days	Sat 24/11/30	Fri 25/1/3	Sat 24/11/30	Fri 25/1/3	Sat 24/11/30	Fri 25/1/3	0 days	2	88FS-15 days,8
94	Excavation and Lateral Support	NA	As Possible	35 days	Tue 24/12/17	Mon 25/1/20	Tue 24/12/17	Mon 25/1/20	Tue 24/12/17	Mon 25/1/20	0 days	2	93FS-18 days
95	**Ground and Edge Beams**	**NA**	**As Possible**	**69 days**	**Fri 25/1/3**	**Wed 25/3/12**	**Fri 25/1/3**	**Wed 25/3/12**	**Fri 25/1/3**	**Wed 25/3/12**	**0 days**		
96	Install precast portion	NA	As Possible	40 days	Fri 25/1/3	Tue 25/2/11	Fri 25/1/3	Tue 25/2/11	Fri 25/1/3	Tue 25/2/11	0 days	0	94FS-18 days
97	Rebar Fixing	NA	As Possible	35 days	Mon 25/1/20	Sun 25/2/23	Mon 25/1/20	Sun 25/2/23	Mon 25/1/20	Sun 25/2/23	0 days	2	96FS-23 days
98	Formwork Erection and Cast-in items	NA	As Possible	35 days	Thu 25/2/6	Wed 25/3/12	Thu 25/2/6	Wed 25/3/12	Thu 25/2/6	Wed 25/3/12	0 days	2	97FS-18 days
99	Concreting	NA	As Possible	14 days	Sun 25/2/23	Sat 25/3/8	Sun 25/2/23	Sat 25/3/8	Sun 25/2/23	Sat 25/3/8	0 days	0	98FS-18 days
100	**Walls**	**NA**	**As Possible**	**52 days**	**Sun 25/3/9**	**Tue 25/4/29**	**Sun 25/3/9**	**Tue 25/4/29**	**Sun 25/3/9**	**Tue 25/4/29**	**0 days**		

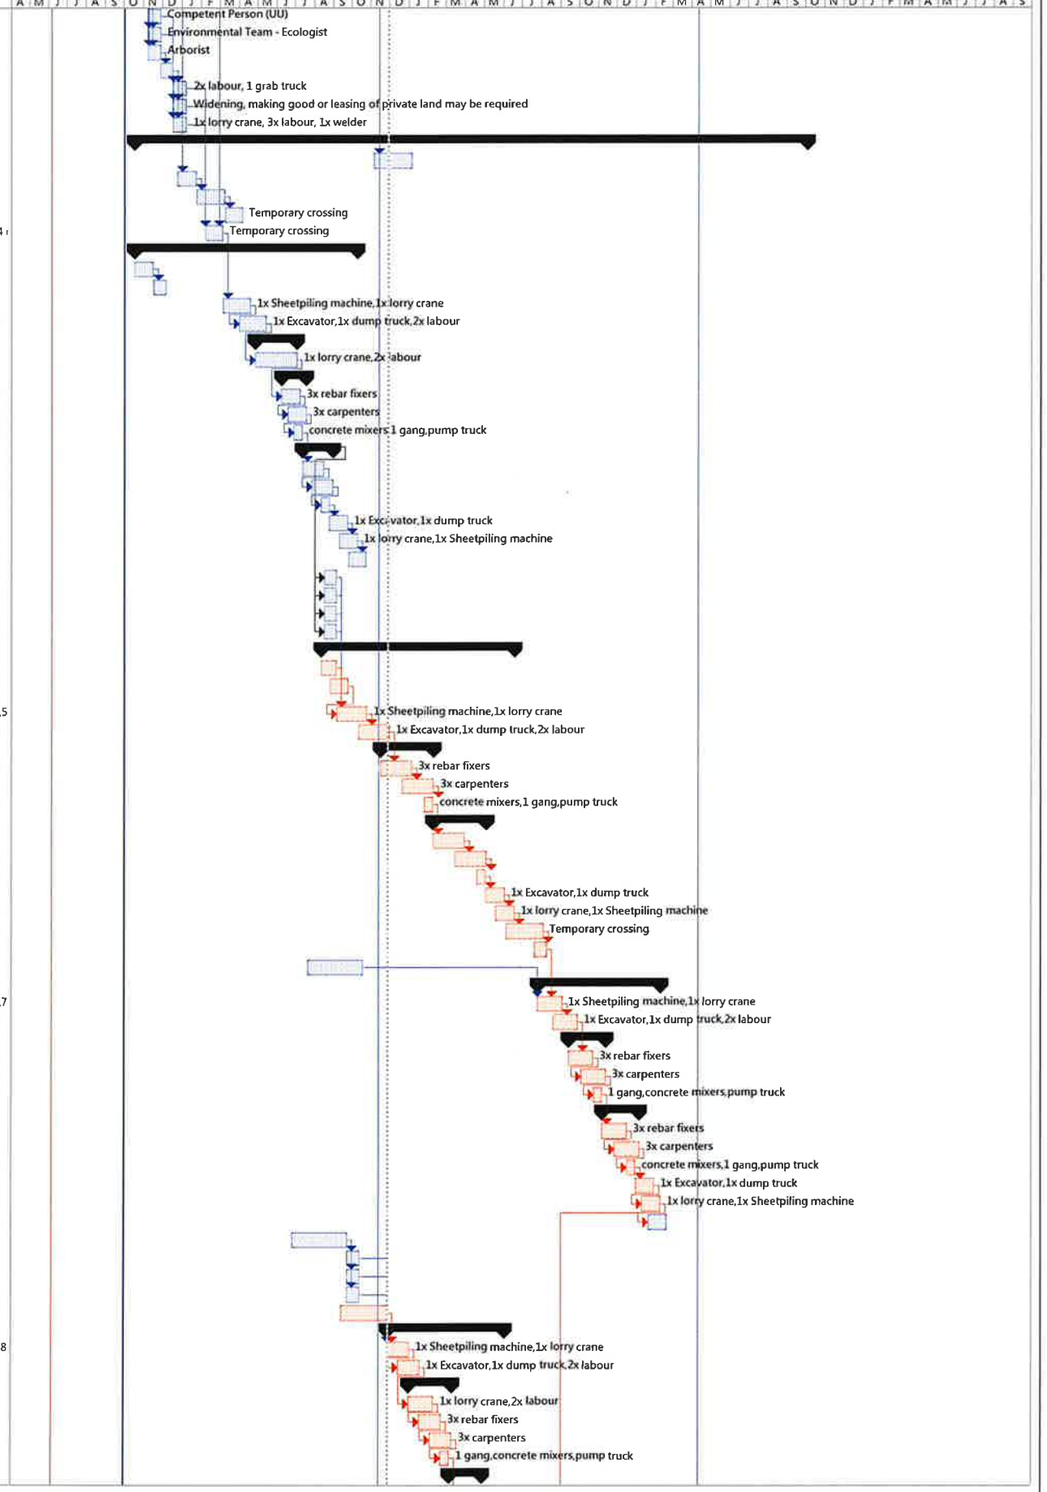


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
101	Rebar Fixing	NA	As Possible	35 days	Sun 25/3/9	Sat 25/4/12	Sun 25/3/9	Sat 25/4/12	Sun 25/3/9	Sat 25/4/12	0 days	2	99
102	Formwork Erection and Cast-in items	NA	As Possible	35 days	Wed 25/3/26	Tue 25/4/29	Wed 25/3/26	Tue 25/4/29	Wed 25/3/26	Tue 25/4/29	0 days	2	101FS-18 days
103	Concreting	NA	As Possible	14 days	Sat 25/4/12	Fri 25/4/25	Sat 25/4/12	Fri 25/4/25	Sat 25/4/12	Fri 25/4/25	0 days	0	102FS-18 days
104	Backfilling and Compaction	NA	As Possible	30 days	Sat 25/4/26	Sun 25/5/25	Sat 25/4/26	Sun 25/5/25	Sat 25/4/26	Sun 25/5/25	0 days	0	103
105	Removal of Sheetpiles	NA	As Possible	30 days	Tue 25/5/6	Wed 25/6/4	Tue 25/5/6	Wed 25/6/4	Tue 25/5/6	Wed 25/6/4	0 days	0	104FS-20 days
106	Temp support to 3x ex. Cable bridge	########	Later Than	60 days	Fri 25/5/16	Mon 25/7/14	Fri 25/5/16	Mon 25/7/14	Fri 26/8/7	Mon 26/10/5	448 days	4	105FS-20 days
107	Demolish & relocate porch YLL797/34,37	NA	As Possible	20 days	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	0 days	0	105FS-20 days
108	Demolish & relocate car body YLL797/36	NA	As Possible	20 days	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	0 days	0	105FS-20 days
109	Demolish & relocate godown YLL797/35	NA	As Possible	20 days	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	Fri 25/5/16	Wed 25/6/4	0 days	0	105FS-20 days
110	**HC07 CH.A400.00~CH.A500.00**	**NA**	**As Possible**	**187 days**	**Wed 25/5/21**	**Sun 25/11/23**	**Wed 25/5/21**	**Sun 25/11/23**	**Wed 25/5/21**	**Sun 25/11/23**	**0 days**		
111	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	35 days	Wed 25/5/21	Tue 25/6/24	Wed 25/5/21	Tue 25/6/24	Wed 25/5/21	Tue 25/6/24	0 days	2	107FS-15 days,
112	Excavation and Lateral Support	NA	As Possible	35 days	Sat 25/6/7	Fri 25/7/11	Sat 25/6/7	Fri 25/7/11	Sat 25/6/7	Fri 25/7/11	0 days	2	111FS-18 days
113	**Ground and Edge Beams**	**NA**	**As Possible**	**69 days**	**Tue 25/6/24**	**Sun 25/8/31**	**Tue 25/6/24**	**Sun 25/8/31**	**Tue 25/6/24**	**Sun 25/8/31**	**0 days**		
114	Install precast portion	NA	As Possible	40 days	Tue 25/6/24	Sat 25/8/2	Tue 25/6/24	Sat 25/8/2	Tue 25/6/24	Sat 25/8/2	0 days	0	112FS-18 days
115	Rebar Fixing	NA	As Possible	35 days	Fri 25/7/11	Thu 25/8/14	Fri 25/7/11	Thu 25/8/14	Fri 25/7/11	Thu 25/8/14	0 days	2	114FS-23 days
116	Formwork Erection and Cast-in items	NA	As Possible	35 days	Mon 25/7/28	Sun 25/8/31	Mon 25/7/28	Sun 25/8/31	Mon 25/7/28	Sun 25/8/31	0 days	2	115FS-18 days
117	Concreting	NA	As Possible	14 days	Thu 25/8/14	Wed 25/8/27	Thu 25/8/14	Wed 25/8/27	Thu 25/8/14	Wed 25/8/27	0 days	0	116FS-18 days
118	**Walls**	**NA**	**As Possible**	**52 days**	**Thu 25/8/28**	**Sat 25/10/18**	**Thu 25/8/28**	**Sat 25/10/18**	**Thu 25/8/28**	**Sat 25/10/18**	**0 days**		
119	Rebar Fixing	NA	As Possible	35 days	Thu 25/8/28	Wed 25/10/1	Thu 25/8/28	Wed 25/10/1	Thu 25/8/28	Wed 25/10/1	0 days	2	117
120	Formwork Erection and Cast-in items	NA	As Possible	35 days	Sun 25/9/14	Sat 25/10/18	Sun 25/9/14	Sat 25/10/18	Sun 25/9/14	Sat 25/10/18	0 days	2	119FS-18 days
121	Concreting	NA	As Possible	14 days	Wed 25/10/1	Tue 25/10/14	Wed 25/10/1	Tue 25/10/14	Wed 25/10/1	Tue 25/10/14	0 days	0	120FS-18 days
122	Backfilling and Compaction	NA	As Possible	30 days	Wed 25/10/15	Thu 25/11/13	Wed 25/10/15	Thu 25/11/13	Wed 25/10/15	Thu 25/11/13	0 days	0	121
123	Removal of Sheetpiles	NA	As Possible	30 days	Sat 25/10/25	Sun 25/11/23	Sat 25/10/25	Sun 25/11/23	Sat 25/10/25	Sun 25/11/23	0 days	0	122FS-20 days
124	Demolish & relocate porch, hoarding YLL797/44	NA	As Possible	20 days	Tue 25/11/4	Sun 25/11/23	Tue 25/11/4	Sun 25/11/23	Tue 25/11/4	Sun 25/11/23	0 days	0	123FS-20 days
125	Demolish & relocate porch YLL797/38,39	NA	As Possible	20 days	Tue 25/11/4	Sun 25/11/23	Tue 25/11/4	Sun 25/11/23	Tue 25/11/4	Sun 25/11/23	0 days	0	123FS-20 days
126	**HC08 CH.A500.00~CH.A546.816**	**NA**	**As Possible**	**170 days**	**Sun 25/11/9**	**Mon 26/4/27**	**Sun 25/11/9**	**Mon 26/4/27**	**Sun 25/11/9**	**Mon 26/4/27**	**0 days**		
127	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	30 days	Sun 25/11/9	Mon 25/12/8	Sun 25/11/9	Mon 25/12/8	Sun 25/11/9	Mon 25/12/8	0 days	2	124FS-15 days,
128	Excavation and Lateral Support	NA	As Possible	30 days	Mon 25/11/24	Tue 25/12/23	Mon 25/11/24	Tue 25/12/23	Mon 25/11/24	Tue 25/12/23	0 days	2	127FS-15 days
129	**Ground and Edge Beams**	**NA**	**As Possible**	**65 days**	**Tue 25/12/9**	**Wed 26/2/11**	**Tue 25/12/9**	**Wed 26/2/11**	**Tue 25/12/9**	**Wed 26/2/11**	**0 days**		
130	Install precast portion	NA	As Possible	40 days	Tue 25/12/9	Sat 26/1/17	Tue 25/12/9	Sat 26/1/17	Tue 25/12/9	Sat 26/1/17	0 days	0	128FS-15 days
131	Rebar Fixing	NA	As Possible	30 days	Mon 25/12/29	Tue 26/1/27	Mon 25/12/29	Tue 26/1/27	Mon 25/12/29	Tue 26/1/27	0 days	2	130FS-20 days
132	Formwork Erection and Cast-in items	NA	As Possible	30 days	Tue 26/1/13	Wed 26/2/11	Tue 26/1/13	Wed 26/2/11	Tue 26/1/13	Wed 26/2/11	0 days	2	131FS-15 days
133	Concreting	NA	As Possible	10 days	Wed 26/1/28	Fri 26/2/6	Wed 26/1/28	Fri 26/2/6	Wed 26/1/28	Fri 26/2/6	0 days	0	132FS-15 days
134	**Walls**	**NA**	**As Possible**	**45 days**	**Sat 26/2/7**	**Mon 26/3/23**	**Sat 26/2/7**	**Mon 26/3/23**	**Sat 26/2/7**	**Mon 26/3/23**	**0 days**		
135	Rebar Fixing	NA	As Possible	30 days	Sat 26/2/7	Sun 26/3/8	Sat 26/2/7	Sun 26/3/8	Sat 26/2/7	Sun 26/3/8	0 days	2	133
136	Formwork Erection and Cast-in items	NA	As Possible	30 days	Sun 26/2/22	Mon 26/3/23	Sun 26/2/22	Mon 26/3/23	Sun 26/2/22	Mon 26/3/23	0 days	2	135FS-15 days
137	Concreting	NA	As Possible	10 days	Mon 26/3/9	Wed 26/3/18	Mon 26/3/9	Wed 26/3/18	Mon 26/3/9	Wed 26/3/18	0 days	0	136FS-15 days
138	Backfilling and Compaction	NA	As Possible	30 days	Thu 26/3/19	Fri 26/4/17	Thu 26/3/19	Fri 26/4/17	Thu 26/3/19	Fri 26/4/17	0 days	0	137
139	Removal of Sheetpiles	NA	As Possible	30 days	Sun 26/3/29	Mon 26/4/27	Sun 26/3/29	Mon 26/4/27	Sun 26/3/29	Mon 26/4/27	0 days	0	138FS-20 days
140	Pedestrian & Vehicular Crossing no. 3 (Box Culvert no. 4)	########	Later Than	60 days	Wed 26/4/8	Sat 26/6/6	Wed 26/4/8	Sat 26/6/6	Fri 26/8/7	Mon 26/10/5	121 days	4	139FS-20 days
141	Demolish & relocate hoarding, wall YLL797/40	NA	As Possible	20 days	Wed 26/4/8	Mon 26/4/27	Wed 26/4/8	Mon 26/4/27	Wed 26/4/8	Mon 26/4/27	0 days	0	139FS-20 days
142	Demolish & relocate storage YLL797/42	NA	As Possible	20 days	Wed 26/4/8	Mon 26/4/27	Wed 26/4/8	Mon 26/4/27	Wed 26/4/8	Mon 26/4/27	0 days	0	139FS-20 days
143	**HC09 CH.A546.816~CH.A611.404**	**NA**	**As Possible**	**155 days**	**Mon 26/4/13**	**Mon 26/9/14**	**Mon 26/4/13**	**Mon 26/9/14**	**Mon 26/4/13**	**Mon 26/9/14**	**0 days**		
144	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	30 days	Mon 26/4/13	Tue 26/5/12	Mon 26/4/13	Tue 26/5/12	Mon 26/4/13	Tue 26/5/12	0 days	1	141FS-15 days,
145	Excavation and Lateral Support	NA	As Possible	30 days	Tue 26/4/28	Wed 26/5/27	Tue 26/4/28	Wed 26/5/27	Tue 26/4/28	Wed 26/5/27	0 days	1	144FS-15 days
146	**Base Slab**	**NA**	**As Possible**	**45 days**	**Wed 26/5/13**	**Fri 26/6/26**	**Wed 26/5/13**	**Fri 26/6/26**	**Wed 26/5/13**	**Fri 26/6/26**	**0 days**		
147	Rebar Fixing	NA	As Possible	30 days	Wed 26/5/13	Thu 26/6/11	Wed 26/5/13	Thu 26/6/11	Wed 26/5/13	Thu 26/6/11	0 days	1	145FS-15 days
148	Formwork Erection and Cast-in items	NA	As Possible	30 days	Thu 26/5/28	Fri 26/6/26	Thu 26/5/28	Fri 26/6/26	Thu 26/5/28	Fri 26/6/26	0 days	1	147FS-15 days
149	Concreting	NA	As Possible	10 days	Fri 26/6/12	Sun 26/6/21	Fri 26/6/12	Sun 26/6/21	Fri 26/6/12	Sun 26/6/21	0 days	0	148FS-15 days
150	**Walls and Roof Slab**	**NA**	**As Possible**	**45 days**	**Mon 26/6/22**	**Wed 26/8/5**	**Mon 26/6/22**	**Wed 26/8/5**	**Mon 26/6/22**	**Wed 26/8/5**	**0 days**		
151	Rebar Fixing	NA	As Possible	30 days	Mon 26/6/22	Tue 26/7/21	Mon 26/6/22	Tue 26/7/21	Mon 26/6/22	Tue 26/7/21	0 days	1	149
152	Formwork Erection and Cast-in items	NA	As Possible	30 days	Tue 26/7/7	Wed 26/8/5	Tue 26/7/7	Wed 26/8/5	Tue 26/7/7	Wed 26/8/5	0 days	1	151FS-15 days
153	Concreting	NA	As Possible	10 days	Wed 26/7/22	Fri 26/7/31	Wed 26/7/22	Fri 26/7/31	Wed 26/7/22	Fri 26/7/31	0 days	0	152FS-15 days
154	Backfilling and Compaction	NA	As Possible	30 days	Sat 26/8/1	Sun 26/8/30	Sat 26/8/1	Sun 26/8/30	Sat 26/8/1	Sun 26/8/30	0 days	0	153
155	Removal of Sheetpiles	NA	As Possible	30 days	Sun 26/8/16	Mon 26/9/14	Sun 26/8/16	Mon 26/9/14	Sun 26/8/16	Mon 26/9/14	0 days	0	154FS-15 days
156	Facing stone	########	Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	155
157	ABWF works	########	Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	155
158	Bedding works	########	Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	155
159	**Drainage Channel Works (West)**	**NA**	**As Possible**	**697 days**	**Fri 24/11/8**	**Mon 26/10/5**	**Fri 24/11/8**	**Mon 26/10/5**	**Fri 25/9/19**	**Mon 26/10/5**	**0 days**		
160	HC11 CH.A674.419~CH.A740.619 (Ex. CH Str. Assessment)	########	Later Than	60 days	Fri 24/11/8	Mon 25/1/6	Fri 24/11/8	Mon 25/1/6	Fri 26/8/7	Mon 26/10/5	637 days	0	19
161	Demolish ex. Geotechnical feature 6NE-B/R19	NA	As Possible	25 days	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	0 days	0	85FS-145 days
162	Demolish ex. Geotechnical feature 6NE-B/R19	NA	As Possible	25 days	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	0 days	0	85FS-145 days
163	Demolish & relocate boundary wall, platform, gate YLL797/46	NA	As Possible	25 days	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	Fri 25/9/19	Mon 25/10/13	0 days	0	85FS-145 days
164	**HC12 CH.A740.619~CH.A863.619**	**NA**	**As Possible**	**211 days**	**Mon 25/9/29**	**Mon 26/4/27**	**Mon 25/9/29**	**Mon 26/4/27**	**Mon 25/9/29**	**Mon 26/4/27**	**0 days**		
165	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	50 days	Mon 25/9/29	Mon 25/11/17	Mon 25/9/29	Mon 25/11/17	Mon 25/9/29	Mon 25/11/17	0 days	2	161FS-15 days,
166	Excavation and Lateral Support	NA	As Possible	50 days	Fri 25/10/24	Fri 25/12/12	Fri 25/10/24	Fri 25/12/12	Fri 25/10/24	Fri 25/12/12	0 days	2	165FS-25 days
167	**Ground and Edge Beams**	**NA**	**As Possible**	**77 days**	**Tue 25/11/18**	**Mon 26/2/2**	**Tue 25/11/18**	**Mon 26/2/2**	**Tue 25/11/18**	**Mon 26/2/2**	**0 days**		
168	Install precast portion	NA	As Possible	50 days	Tue 25/11/18	Tue 26/1/6	Tue 25/11/18	Tue 26/1/6	Tue 25/11/18	Tue 26/1/6	0 days	0	166FS-25 days
169	Rebar Fixing	NA	As Possible	35 days	Sat 25/12/13	Fri 26/1/16	Sat 25/12/13	Fri 26/1/16	Sat 25/12/13	Fri 26/1/16	0 days	2	168FS-25 days
170	Formwork Erection and Cast-in items	NA	As Possible	35 days	Tue 25/12/30	Mon 26/2/2	Tue 25/12/30	Mon 26/2/2	Tue 25/12/30	Mon 26/2/2	0 days	2	169FS-18 days
171	Concreting	NA	As Possible	14 days	Fri 26/1/16	Thu 26/1/29	Fri 26/1/16	Thu 26/1/29	Fri 26/1/16	Thu 26/1/29	0 days	0	170FS-18 days
172	**Walls**	**NA**	**As Possible**	**52 days**	**Fri 26/1/30**	**Sun 26/3/22**	**Fri 26/1/30**	**Sun 26/3/22**	**Fri 26/1/30**	**Sun 26/3/22**	**0 days**		
173	Rebar Fixing	NA	As Possible	35 days	Fri 26/1/30	Thu 26/3/5	Fri 26/1/30	Thu 26/3/5	Fri 26/1/30	Thu 26/3/5	0 days	2	171
174	Formwork Erection and Cast-in items	NA	As Possible	35 days	Mon 26/2/16	Sun 26/3/22	Mon 26/2/16	Sun 26/3/22	Mon 26/2/16	Sun 26/3/22	0 days	2	173FS-18 days
175	Concreting	NA	As Possible	14 days	Thu 26/3/5	Wed 26/3/18	Thu 26/3/5	Wed 26/3/18	Thu 26/3/5	Wed 26/3/18	0 days	0	174FS-18 days
176	Backfilling and Compaction	NA	As Possible	30 days	Thu 26/3/19	Fri 26/4/17	Thu 26/3/19	Fri 26/4/17	Thu 26/3/19	Fri 26/4/17	0 days	0	175
177	Removal of Sheetpiles	NA	As Possible	30 days	Sun 26/3/29	Mon 26/4/27	Sun 26/3/29	Mon 26/4/27	Sun 26/3/29	Mon 26/4/27	0 days	0	176FS-20 days
178	**HC13 CH.A863.619~CH.A905.630**	**NA**	**As Possible**	**180 days**	**Wed 26/4/8**	**Sun 26/10/4**	**Wed 26/4/8**	**Sun 26/10/4**	**Wed 26/4/8**	**Sun 26/10/4**	**0 days**		
179	Sheetpiling & Temp. Drainage Diversion	NA	As Possible	50 days	Wed 26/4/8	Wed 26/5/27	Wed 26/4/8	Wed 26/5/27	Wed 26/4/8	Wed 26/5/27	0 days	2	177FS-20 days
180	Excavation and Lateral Support	NA	As Possible	50 days	Sun 26/5/3	Sun 26/6/21	Sun 26/5/3	Sun 26/6/21	Sun 26/5/3	Sun 26/6/21	0 days	2	179FS-25 days
181	**Ground and Edge Beams**	**NA**	**As Possible**	**65 days**	**Thu 26/5/28**	**Fri 26/7/31**	**Thu 26/5/28**	**Fri 26/7/31**	**Thu 26/5/28**	**Fri 26/7/31**	**0 days**		
182	Install precast portion (ground beam)	NA	As Possible	40 days	Thu 26/5/28	Mon 26/7/6	Thu 26/5/28	Mon 26/7/6	Thu 26/5/28	Mon 26/7/6	0 days	0	180FS-25 days

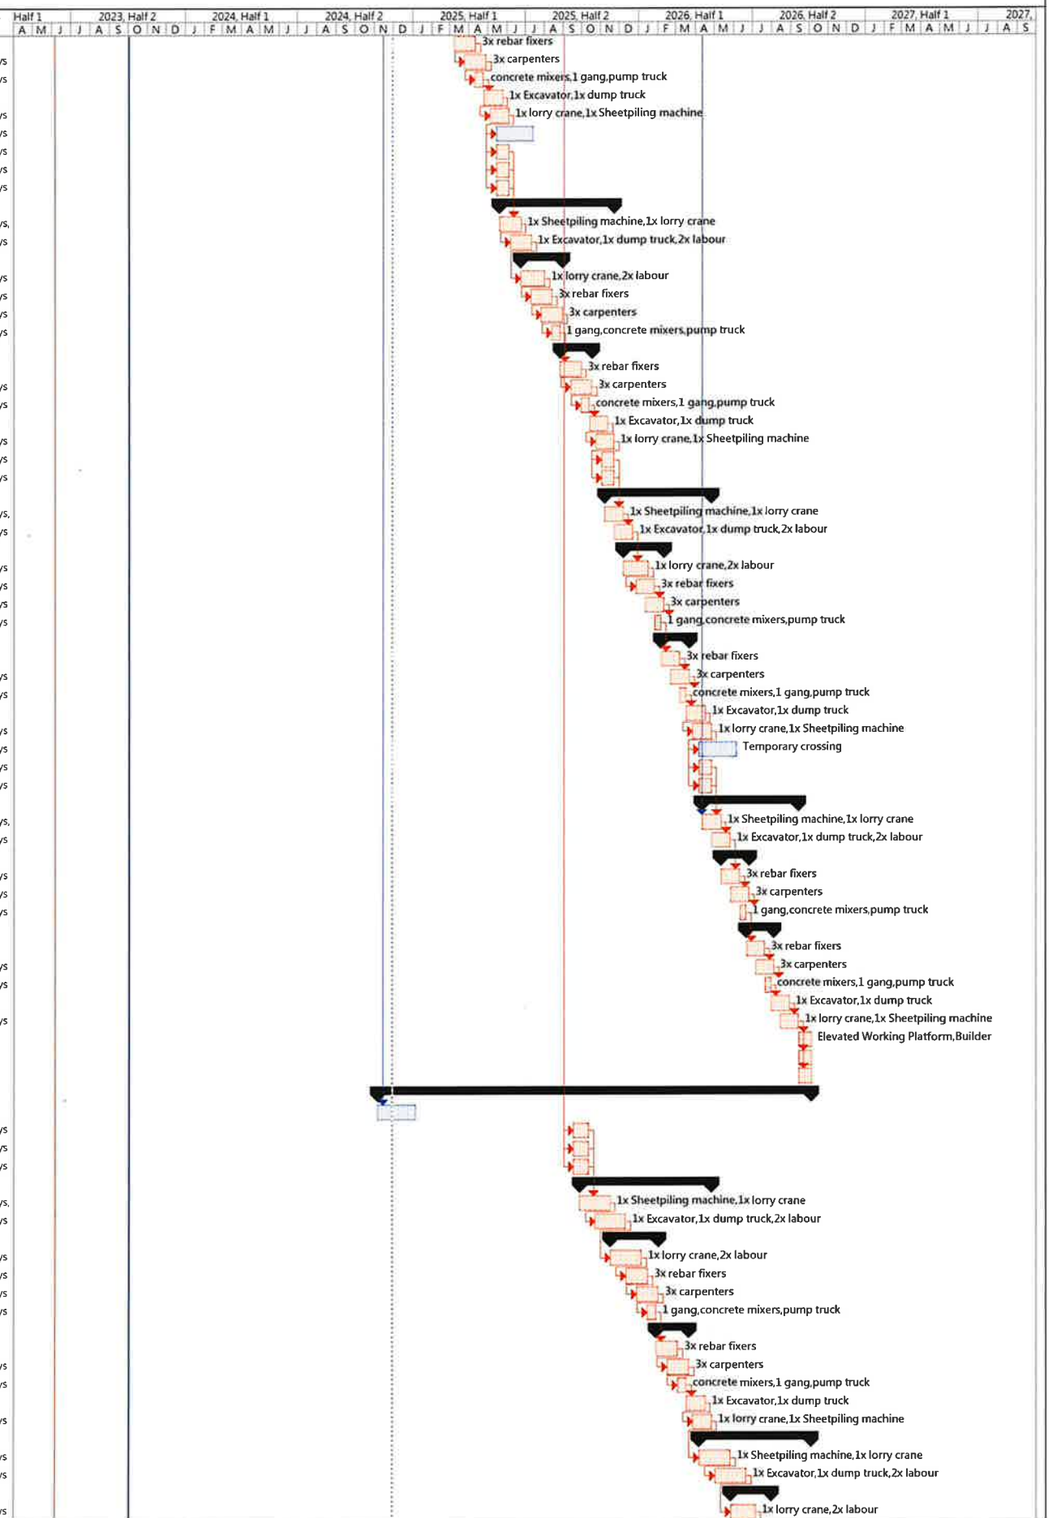


Revision : 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
183	Rebar Fixing	NA	As Possible	30 days	Wed 26/6/17	Thu 26/7/16	Wed 26/6/17	Thu 26/7/16	Wed 26/6/17	Thu 26/7/16	0 days	2	182FS-20 days
184	Formwork Erection and Cast-in items	NA	As Possible	30 days	Thu 26/7/2	Fri 26/7/31	Thu 26/7/2	Fri 26/7/31	Thu 26/7/2	Fri 26/7/31	0 days	2	183FS-15 days
185	Concreting	NA	As Possible	10 days	Fri 26/7/17	Sun 26/7/26	Fri 26/7/17	Sun 26/7/26	Fri 26/7/17	Sun 26/7/26	0 days	0	184FS-15 days
186	**Walls**	NA	As Possible	**30 days**	**Mon 26/7/27**	**Tue 26/8/25**	**Mon 26/7/27**	**Tue 26/8/25**	**Mon 26/7/27**	**Tue 26/8/25**	**0 days**		
187	Rebar Fixing	NA	As Possible	20 days	Mon 26/7/27	Sat 26/8/15	Mon 26/7/27	Sat 26/8/15	Mon 26/7/27	Sat 26/8/15	0 days	2	185
188	Formwork Erection and Cast-in items	NA	As Possible	20 days	Thu 26/8/6	Tue 26/8/25	Thu 26/8/6	Tue 26/8/25	Thu 26/8/6	Tue 26/8/25	0 days	2	187FS-10 days
189	Concreting	NA	As Possible	10 days	Sun 26/8/16	Tue 26/8/25	Sun 26/8/16	Tue 26/8/25	Sun 26/8/16	Tue 26/8/25	0 days	0	188FS-10 days
190	Backfilling and Compaction	NA	As Possible	30 days	Wed 26/8/26	Thu 26/9/24	Wed 26/8/26	Thu 26/9/24	Wed 26/8/26	Thu 26/9/24	0 days	0	189
191	Removal of Sheetpiles	NA	As Possible	30 days	Sat 26/9/5	Sun 26/10/4	Sat 26/9/5	Sun 26/10/4	Sat 26/9/5	Sun 26/10/4	0 days	0	190FS-20 days
192	Facing stone	########	o Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	191FS-20 days
193	ABWF works	########	o Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	191FS-20 days
194	Bedding works	########	o Later Than	21 days	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	Tue 26/9/15	Mon 26/10/5	0 days	0	191FS-20 days
114													
115	**Section VII**	NA	As Possible	**820 days**	**Tue 23/5/30**	**Tue 25/8/26**	**Tue 23/5/30**	**Tue 25/8/26**	**Tue 23/5/30**	**Fri 27/4/2**	**0 days**		
2	access date of Portion D	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	Tue 23/5/30	Mon 23/12/25	0 days	0	\\WingTatNasC
3	section VII (Ha Che - Fam Kam Road)	Tue 25/8/26	o Later Than	820 days	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	Tue 23/5/30	Tue 25/8/26	0 days	0	\\WingTatNasC
4	**Site Establishment**	NA	As Possible	**389 days**	**Tue 23/9/12**	**Fri 24/10/4**	**Tue 23/9/12**	**Fri 24/10/4**	**Fri 23/9/22**	**Fri 27/4/2**	**10 days**		
5	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	104 days	Tue 23/9/12	Sun 23/12/24	Tue 23/9/12	Sun 23/12/24	Fri 23/9/22	Wed 24/1/3	10 days	0	\\WingTatNasC
6	Initial Survey	NA	As Possible	285 days	Mon 23/12/25	Fri 24/10/4	Mon 23/12/25	Fri 24/10/4	Thu 24/1/4	Mon 24/10/14	10 days	0	2FS-1 day,5
8	Initial Safety & Environmental measures	NA	As Possible	91 days	Mon 23/12/25	Sun 24/3/24	Mon 23/12/25	Sun 24/3/24	Mon 26/7/6	Sun 26/10/4	924 days	0	2FS-1 day,5
9	Setup of instrumentation and monitoring	NA	As Possible	60 days	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	Mon 26/10/5	Thu 26/12/3	924 days	0	8
10	Tree Survey [A]	NA	As Possible	60 days	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	Mon 26/10/5	Thu 26/12/3	924 days	0	8
11	Condition Survey	NA	As Possible	60 days	Fri 24/5/24	Mon 24/7/22	Fri 24/5/24	Mon 24/7/22	Tue 27/2/2	Fri 27/4/2	984 days	0	9,10
12	UU detection	NA	As Possible	60 days	Fri 24/5/24	Mon 24/7/22	Fri 24/5/24	Mon 24/7/22	Fri 26/12/4	Mon 27/2/1	924 days	0	9,10
13	Site Clearance	NA	As Possible	60 days	Tue 24/7/23	Fri 24/9/20	Tue 24/7/23	Fri 24/9/20	Tue 27/2/2	Fri 27/4/2	924 days	0	12
14	**Temporary Traffic Arrangement**	NA	As Possible	**281 days**	**Mon 23/12/25**	**Mon 24/9/30**	##########	**Mon 24/9/30**	##########	**Mon 24/9/30**	**0 days**		
15	Application of XP	NA	As Possible	251 days	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	0 days	0	2FS-1 day
16	Submission of TTA and Arrange TMLG [A]	NA	As Possible	251 days	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	0 days	0	2FS-1 day
17	Approval of TTA [A]	NA	As Possible	30 days	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	0 days	0	15,16
18	**Drain Laying Works**	NA	As Possible	**684 days**	**Fri 23/10/13**	**Tue 25/8/26**	**Fri 23/10/13**	**Tue 25/8/26**	**Fri 23/10/13**	**Tue 25/8/26**	**0 days**		
19	[PMI022] Alternative methodology design for drainage channel underneath Fan Kam Road (impact to be ascertained)	Fri 23/10/13	Start No Earlier Than	324 days	Fri 23/10/13	Sat 24/8/31	Fri 23/10/13	Sat 24/8/31	Fri 23/10/13	Sat 24/8/31	0 days	0	
20	Acceptance of alternative methodology and protection method to ex. Dongjiang Watermain [A]	NA	As Soon As Possible	30 days	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	0 days	0	19
21	Protection to ex. Dongjiang Water Main [A]	NA	As Possible	14 days	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	Tue 24/10/1	Mon 24/10/14	0 days	0	17,20
22	**HC10 CH.A611.404~CH.A674.419 (Fan Kam Road)**	NA	As Possible	**286 days**	**Tue 24/10/15**	**Sun 25/7/27**	**Tue 24/10/15**	**Sun 25/7/27**	**Tue 24/10/15**	**Sun 25/7/27**	**0 days**		
23	N/B TTA implementation [A]	NA	As Possible	7 days	Tue 24/10/15	Mon 24/10/21	Tue 24/10/15	Mon 24/10/21	Tue 24/10/15	Mon 24/10/21	0 days	0	21,17,6
24	Sheet Piles installation	NA	As Possible	15 days	Tue 24/10/22	Tue 24/11/5	Tue 24/10/22	Tue 24/11/5	Tue 24/10/22	Tue 24/11/5	0 days	0	23
25	Construction of top slab	NA	As Possible	32 days	Wed 24/11/6	Sat 24/12/7	Wed 24/11/6	Sat 24/12/7	Wed 24/11/6	Sat 24/12/7	0 days	0	24
26	Backfilling and reinstatement	NA	As Possible	15 days	Sun 24/12/8	Sun 24/12/22	Sun 24/12/8	Sun 24/12/22	Sun 24/12/8	Sun 24/12/22	0 days	0	25
27	S/B TTA implementation	NA	As Possible	7 days	Mon 24/12/23	Sun 24/12/29	Mon 24/12/23	Sun 24/12/29	Mon 24/12/23	Sun 24/12/29	0 days	0	26
28	Sheet Piles installation	NA	As Possible	15 days	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	0 days	0	27
29	Construction of top slab	NA	As Possible	32 days	Tue 25/1/14	Fri 25/2/14	Tue 25/1/14	Fri 25/2/14	Tue 25/1/14	Fri 25/2/14	0 days	0	28
30	Backfilling and reinstatement	NA	As Possible	15 days	Sat 25/2/15	Sat 25/3/1	Sat 25/2/15	Sat 25/3/1	Sat 25/2/15	Sat 25/3/1	0 days	0	29
31	Demolition of existing culvert & install temp. support	NA	As Possible	60 days	Sun 25/3/2	Wed 25/4/30	Sun 25/3/2	Wed 25/4/30	Sun 25/3/2	Wed 25/4/30	0 days	0	30
32	Construction of alternative box-culvert	NA	As Possible	60 days	Thu 25/5/1	Sun 25/6/29	Thu 25/5/1	Sun 25/6/29	Thu 25/5/1	Sun 25/6/29	0 days	0	31
33	Removal of temporary support	NA	As Possible	28 days	Mon 25/6/30	Sun 25/7/27	Mon 25/6/30	Sun 25/7/27	Mon 25/6/30	Sun 25/7/27	0 days	0	32
34	CCTV inspection and T&C	Tue 25/8/26	o Later Than	30 days	Mon 25/7/28	Tue 25/8/26	Mon 25/7/28	Tue 25/8/26	Mon 25/7/28	Tue 25/8/26	0 days	0	33
116													
117	**Section V**	NA	As Possible	**1105 days**	**Mon 23/5/29**	**Sat 26/6/6**	**Mon 23/5/29**	**Sat 26/6/6**	**Tue 23/5/30**	**Fri 27/4/2**	**1 day**		
2	access date of Portion E1	########	o Later Than	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Tue 23/6/13	Tue 23/6/13	15 days	0	\\WingTatNasC
3	section V (Shan Ha Tsuen - Shan Ha Road)	########	o Later Than	973 days	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	0 days	0	\\WingTatNasC
4	Planned Completion Day	Mon 26/4/6	o Later Than	70 days	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	0 days	0	3
5	**Site Establishment**	NA	As Possible	**871 days**	**Mon 23/5/29**	**Wed 25/10/15**	**Mon 23/5/29**	**Wed 25/10/15**	**Tue 23/6/13**	**Thu 25/10/30**	**15 days**		
6	Prepare and Accept Temp. Works Design and Method Statement [A]	Mon 26/4/6	o Later Than	751 days	Tue 23/9/26	Wed 25/10/15	Tue 23/9/26	Wed 25/10/15	Wed 23/10/11	Thu 25/10/30	15 days	0	\\WingTatNasC
7	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	104 days	Tue 23/9/12	Sun 23/12/24	Tue 23/9/12	Sun 23/12/24	Mon 23/10/9	Sat 24/1/20	27 days	0	\\WingTatNasC
8	Initial Survey [A]	Mon 26/4/6	o Later Than	871 days	Mon 23/5/29	Wed 25/10/15	Mon 23/5/29	Wed 25/10/15	Tue 23/6/13	Thu 25/10/30	15 days	0	2FS-1 day
9	[EWN011] Objection and additional request of Village Rep.	NA	As Possible	85 days	Mon 23/12/25	Mon 24/3/18	Mon 23/12/25	Mon 24/3/18	Sun 24/1/21	Sun 24/4/14	27 days	0	7
10	[EWN011] Objection and additional request of Village Rep.	NA	As Possible	30 days	Tue 24/3/19	Wed 24/4/17	Tue 24/3/19	Wed 24/4/17	Mon 24/4/15	Tue 24/5/14	27 days	0	9
12	Initial Safety & Environmental measures [A]	NA	As Possible	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Mon 24/4/15	Tue 24/5/14	15 days	0	17FF
14	Setup of instrumentation and monitoring [A]	NA	As Possible	45 days	Sat 24/3/16	Mon 24/4/29	Sat 24/3/16	Mon 24/4/29	Sun 24/3/31	Tue 24/5/14	15 days	0	17FF
15	Tree Survey [A]	NA	As Possible	45 days	Sat 24/3/16	Mon 24/4/29	Sat 24/3/16	Mon 24/4/29	Sun 24/3/31	Tue 24/5/14	15 days	0	17FF
16	UU detection [A]	NA	As Possible	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Mon 24/4/15	Tue 24/5/14	15 days	0	17FF
17	Site Clearance [A]	NA	As Possible	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Mon 24/4/15	Tue 24/5/14	15 days	0	21FF
18	**Temporary Traffic Arrangement**	NA	As Possible	**337 days**	**Mon 23/5/29**	**Mon 24/4/29**	**Mon 23/5/29**	**Mon 24/4/29**	**Tue 23/6/13**	**Tue 24/5/14**	**15 days**		
19	Application of XP [A]	NA	As Possible	307 days	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	Tue 23/6/13	Sun 24/4/14	15 days	0	2FS-1 day
20	Submission of TTA and Arrange TMLG [A]	NA	As Possible	307 days	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	Tue 23/6/13	Sun 24/4/14	15 days	0	2FS-1 day
21	Approval of TTA [A]	NA	As Possible	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Mon 24/4/15	Tue 24/5/14	15 days	0	19,20,9
22	**Drain Laying Works**	NA	As Possible	**692 days**	**Tue 24/4/30**	**Sun 26/3/22**	**Tue 24/4/30**	**Sun 26/3/22**	**Wed 24/5/15**	**Mon 26/4/6**	**15 days**		
23	**SHT.A3A~SHT.A04,1500PC,B,L=49.29,D=3.65**	NA	As Possible	**161 days**	**Tue 24/4/30**	**Mon 24/10/7**	**Tue 24/4/30**	**Mon 24/10/7**	**Wed 24/5/15**	**Tue 24/10/22**	**15 days**		
24	**Stage 1**	NA	As Possible	**83 days**	**Tue 24/4/30**	**Sun 24/7/21**	**Tue 24/4/30**	**Sun 24/7/21**	**Wed 24/5/15**	**Mon 24/8/5**	**15 days**		
25	TTA Implementation (trial run) [A]	NA	As Possible	7 days	Tue 24/4/30	Mon 24/5/6	Tue 24/4/30	Mon 24/5/6	Wed 24/5/15	Tue 24/5/21	15 days	0	17,21,12,14,15,
26	Breaking Ground [A]	NA	As Possible	14 days	Sun 24/5/5	Sat 24/5/18	Sun 24/5/5	Sat 24/5/18	Mon 24/5/20	Sun 24/6/2	15 days	1	25FS-2 days
27	Excavation and Lateral Support [A]	NA	As Possible	20 days	Fri 24/5/17	Wed 24/6/5	Fri 24/5/17	Wed 24/6/5	Sat 24/6/1	Thu 24/6/20	15 days	2	26FS-2 days
28	Drain Laying [A]	NA	As Possible	20 days	Tue 24/6/4	Sun 24/6/23	Tue 24/6/4	Sun 24/6/23	Wed 24/6/19	Mon 24/7/8	15 days	2	27FS-2 days
29	Bedding and Backfilling [A]	NA	As Possible	18 days	Sat 24/6/22	Tue 24/7/9	Sat 24/6/22	Tue 24/7/9	Sun 24/7/7	Wed 24/7/24	15 days	0	28FS-2 days
30	Reinstatement [A]	NA	As Possible	12 days	Mon 24/7/8	Fri 24/7/19	Mon 24/7/8	Fri 24/7/19	Tue 24/7/23	Sat 24/8/3	15 days	0	29FS-2 days
31	TTA Removal [A]	NA	As Possible	2 days	Sat 24/7/20	Sun 24/7/21	Sat 24/7/20	Sun 24/7/21	Sun 24/8/4	Mon 24/8/5	15 days	0	30
32	**Stage 2**	NA	As Possible	**78 days**	**Mon 24/7/22**	**Mon 24/10/7**	**Mon 24/7/22**	**Mon 24/10/7**	**Tue 24/8/6**	**Tue 24/10/22**	**15 days**		
33	TTA Implementation [A]	NA	As Possible	4 days	Mon 24/7/22	Thu 24/7/25	Mon 24/7/22	Thu 24/7/25	Tue 24/8/6	Fri 24/8/9	15 days	0	31
34	Breaking Ground [A]	NA	As Possible	14 days	Wed 24/7/24	Tue 24/8/6	Wed 24/7/24	Tue 24/8/6	Thu 24/8/8	Wed 24/8/21	15 days	1	33FS-2 days
35	Excavation and Lateral Support [A]	NA	As Possible	20 days	Mon 24/8/5	Sat 24/8/24	Mon 24/8/5	Sat 24/8/24	Tue 24/8/20	Sun 24/9/8	15 days	2	34FS-2 days
36	Drain Laying [A]	NA	As Possible	20 days	Fri 24/8/23	Wed 24/9/11	Fri 24/8/23	Wed 24/9/11	Sat 24/9/7	Thu 24/9/26	15 days	2	35FS-2 days

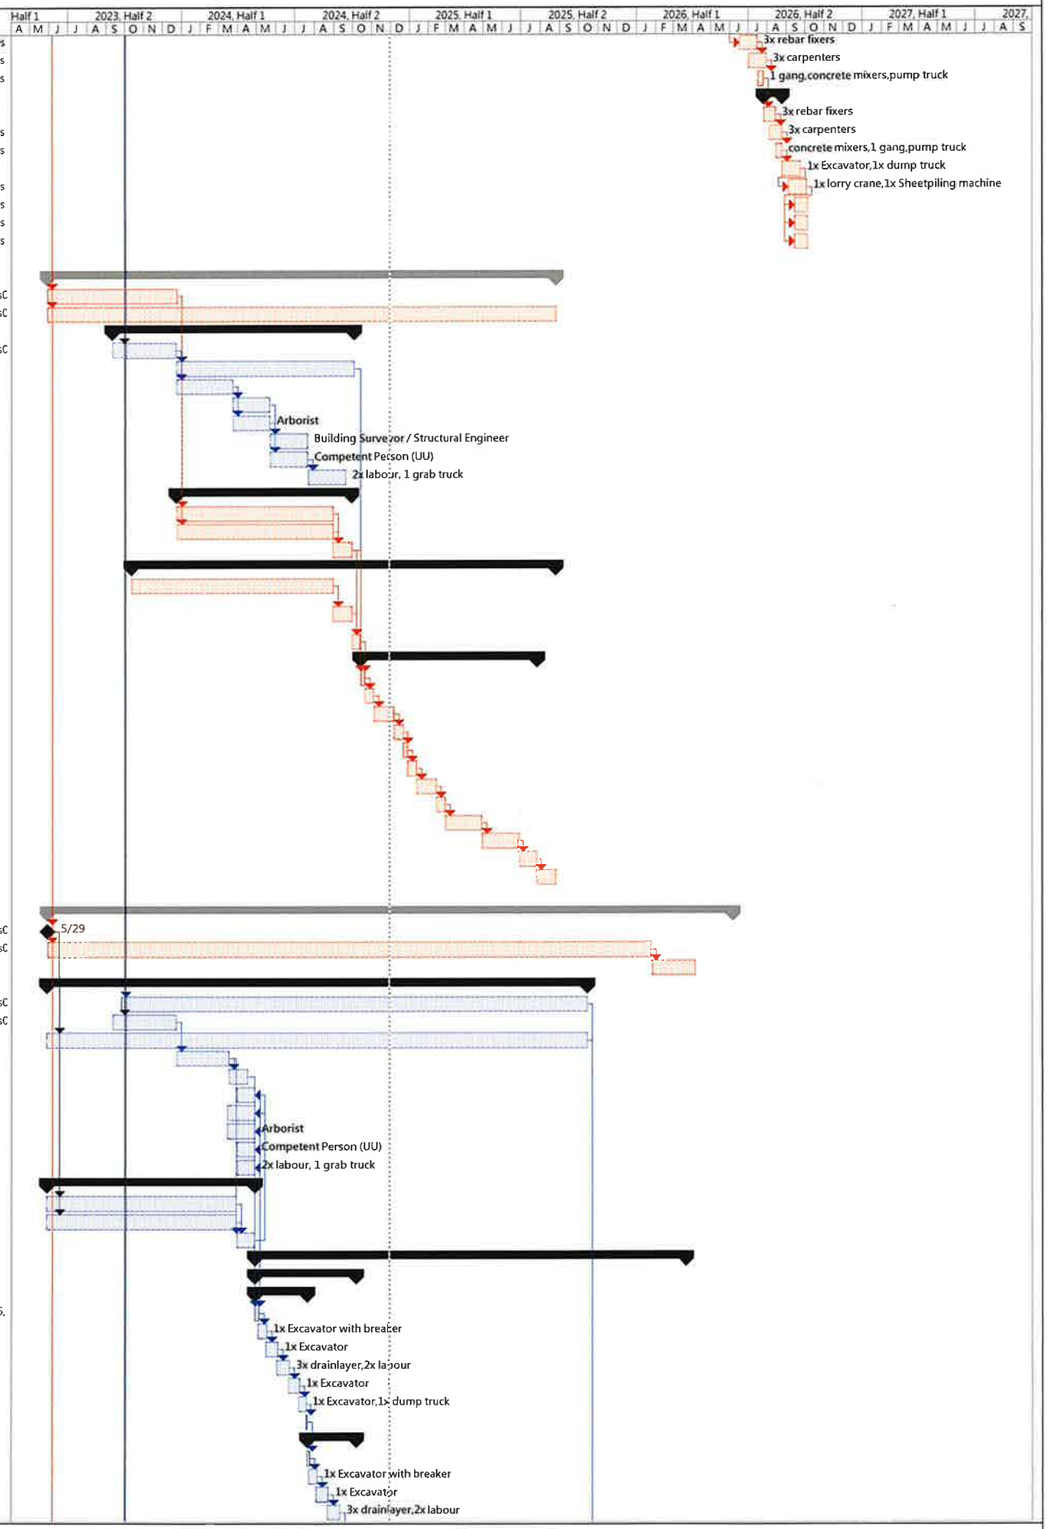


Revision.: 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
37	Bedding and Backfilling [A]	NA	As Possible	16 days	Tue 24/9/10	Wed 24/9/25	Tue 24/9/10	Wed 24/9/25	Wed 24/9/25	Thu 24/10/10	15 days	0	36FS-2 days
38	Reinstatement [A]	NA	As Possible	12 days	Tue 24/9/24	Sat 24/10/5	Tue 24/9/24	Sat 24/10/5	Wed 24/10/9	Sun 24/10/20	15 days	0	37FS-2 days
39	TTA Removal [A]	NA	As Possible	2 days	Sun 24/10/6	Mon 24/10/7	Sun 24/10/6	Mon 24/10/7	Mon 24/10/21	Tue 24/10/22	15 days	0	38
40	SHT.A05~SHT.A06A,1500PC,B,L=13.12,D=3.15	NA	As Possible	66 days	Tue 24/10/8	Thu 24/12/12	Tue 24/10/8	Thu 24/12/12	Wed 24/10/23	Fri 24/12/27	15 days		
41	TTA Implementation [A]	NA	As Possible	4 days	Tue 24/10/8	Fri 24/10/11	Tue 24/10/8	Fri 24/10/11	Wed 24/10/23	Sat 24/10/26	15 days	0	39
42	Breaking Ground [A]	NA	As Possible	14 days	Thu 24/10/10	Wed 24/10/23	Thu 24/10/10	Wed 24/10/23	Fri 24/10/25	Thu 24/11/7	15 days	1	41FS-2 days
43	Excavation and Lateral Support	NA	As Possible	16 days	Tue 24/10/22	Wed 24/11/6	Tue 24/10/22	Wed 24/11/6	Wed 24/11/6	Thu 24/11/21	15 days	2	42FS-2 days
44	Drain Laying	NA	As Possible	14 days	Tue 24/11/5	Mon 24/11/18	Tue 24/11/5	Mon 24/11/18	Wed 24/11/20	Tue 24/12/3	15 days	2	43FS-2 days
45	Bedding and Backfilling	NA	As Possible	8 days	Sun 24/11/17	Sun 24/11/24	Sun 24/11/17	Sun 24/11/24	Mon 24/12/2	Mon 24/12/9	15 days	0	44FS-2 days
46	Manhole Construction	NA	As Possible	10 days	Sat 24/11/23	Mon 24/12/2	Sat 24/11/23	Mon 24/12/2	Sun 24/12/8	Tue 24/12/17	15 days	1	45FS-2 days
47	Reinstatement	NA	As Possible	8 days	Tue 24/12/3	Tue 24/12/10	Tue 24/12/3	Tue 24/12/10	Wed 24/12/18	Wed 24/12/25	15 days	0	46
48	TTA Removal	NA	As Possible	2 days	Wed 24/12/11	Thu 24/12/12	Wed 24/12/11	Thu 24/12/12	Thu 24/12/26	Fri 24/12/27	15 days	0	47
49	SHT.A03~SHT.A3A,1500PC,B,L=8.59,D=3.65	NA	As Possible	82 days	Fri 24/12/13	Tue 25/3/4	Fri 24/12/13	Tue 25/3/4	Sat 24/12/28	Wed 25/3/19	15 days		
50	TTA Implementation	NA	As Possible	4 days	Fri 24/12/13	Mon 24/12/16	Fri 24/12/13	Mon 24/12/16	Sat 24/12/28	Tue 24/12/31	15 days	0	48
51	Breaking Ground	NA	As Possible	14 days	Sun 24/12/15	Sat 24/12/28	Sun 24/12/15	Sat 24/12/28	Mon 24/12/30	Sun 25/1/12	15 days	1	50FS-2 days
52	Excavation and Lateral Support	NA	As Possible	18 days	Fri 24/12/27	Mon 25/1/13	Fri 24/12/27	Mon 25/1/13	Sat 25/1/11	Tue 25/1/28	15 days	2	51FS-2 days
53	Drain Laying	NA	As Possible	14 days	Sun 25/1/12	Sat 25/1/25	Sun 25/1/12	Sat 25/1/25	Mon 25/1/27	Sun 25/2/9	15 days	2	52FS-2 days
54	Bedding and Backfilling	NA	As Possible	10 days	Fri 25/1/24	Sun 25/2/2	Fri 25/1/24	Sun 25/2/2	Sat 25/2/8	Mon 25/2/17	15 days	0	53FS-2 days
55	Manhole Construction	NA	As Possible	20 days	Sat 25/2/1	Thu 25/2/20	Sat 25/2/1	Thu 25/2/20	Sun 25/2/16	Fri 25/3/7	15 days	1	54FS-2 days
56	Reinstatement	NA	As Possible	10 days	Fri 25/2/21	Sun 25/3/2	Fri 25/2/21	Sun 25/3/2	Sat 25/3/8	Mon 25/3/17	15 days	0	55
57	TTA Removal	NA	As Possible	2 days	Mon 25/3/3	Tue 25/3/4	Mon 25/3/3	Tue 25/3/4	Tue 25/3/18	Wed 25/3/19	15 days	0	56
58	SHT.A02~SHT.A03,1500PC,T,L=32.82,D=3.6	NA	As Possible	107 days	Wed 25/3/5	Thu 25/6/19	Wed 25/3/5	Thu 25/6/19	Thu 25/3/20	Fri 25/7/4	15 days		
59	Stage 1	NA	As Possible	55 days	Wed 25/3/5	Mon 25/4/28	Wed 25/3/5	Mon 25/4/28	Thu 25/3/20	Tue 25/5/13	15 days		
60	TTA Implementation	NA	As Possible	4 days	Wed 25/3/5	Sat 25/3/8	Wed 25/3/5	Sat 25/3/8	Thu 25/3/20	Sun 25/3/23	15 days	0	57
61	Breaking Ground	NA	As Possible	10 days	Fri 25/3/7	Sun 25/3/16	Fri 25/3/7	Sun 25/3/16	Sat 25/3/22	Mon 25/3/31	15 days	1	60FS-2 days
62	Excavation and Lateral Support	NA	As Possible	12 days	Sat 25/3/15	Wed 25/3/26	Sat 25/3/15	Wed 25/3/26	Sun 25/3/30	Thu 25/4/10	15 days	2	61FS-2 days
63	Drain Laying	NA	As Possible	11 days	Tue 25/3/25	Fri 25/4/4	Tue 25/3/25	Fri 25/4/4	Wed 25/4/9	Sat 25/4/19	15 days	2	62FS-2 days
64	Bedding and Backfilling	NA	As Possible	8 days	Thu 25/4/3	Thu 25/4/10	Thu 25/4/3	Thu 25/4/10	Fri 25/4/18	Fri 25/4/25	15 days	0	63FS-2 days
65	Manhole Construction	NA	As Possible	10 days	Wed 25/4/9	Fri 25/4/18	Wed 25/4/9	Fri 25/4/18	Thu 25/4/24	Sat 25/5/3	15 days	1	64FS-2 days
66	Reinstatement	NA	As Possible	8 days	Sat 25/4/19	Sat 25/4/26	Sat 25/4/19	Sat 25/4/26	Sun 25/5/4	Sun 25/5/11	15 days	0	65
67	TTA Removal	NA	As Possible	2 days	Sun 25/4/27	Mon 25/4/28	Sun 25/4/27	Mon 25/4/28	Mon 25/5/12	Tue 25/5/13	15 days	0	66
68	Stage 2	NA	As Possible	52 days	Tue 25/4/29	Thu 25/6/19	Tue 25/4/29	Thu 25/6/19	Wed 25/5/14	Fri 25/7/4	15 days		
69	TTA Implementation	NA	As Possible	4 days	Tue 25/4/29	Fri 25/5/2	Tue 25/4/29	Fri 25/5/2	Wed 25/5/14	Sat 25/5/17	15 days	0	67
70	Breaking Ground	NA	As Possible	10 days	Thu 25/5/1	Sat 25/5/10	Thu 25/5/1	Sat 25/5/10	Fri 25/5/16	Sun 25/5/25	15 days	0	69FS-2 days
71	Excavation and Lateral Support	NA	As Possible	11 days	Fri 25/5/9	Mon 25/5/19	Fri 25/5/9	Mon 25/5/19	Sat 25/5/24	Tue 25/6/3	15 days	2	70FS-2 days
72	Drain Laying	NA	As Possible	9 days	Sun 25/5/18	Mon 25/5/26	Sun 25/5/18	Mon 25/5/26	Mon 25/6/2	Tue 25/6/10	15 days	2	71FS-2 days
73	Bedding and Backfilling	NA	As Possible	8 days	Sun 25/5/25	Sun 25/6/1	Sun 25/5/25	Sun 25/6/1	Mon 25/6/9	Mon 25/6/16	15 days	0	72FS-2 days
74	Manhole Construction	NA	As Possible	10 days	Sat 25/5/31	Mon 25/6/9	Sat 25/5/31	Mon 25/6/9	Sun 25/6/15	Tue 25/6/24	15 days	0	73FS-2 days
75	Reinstatement	NA	As Possible	8 days	Tue 25/6/10	Tue 25/6/17	Tue 25/6/10	Tue 25/6/17	Wed 25/6/25	Wed 25/7/2	15 days	0	74
76	TTA Removal	NA	As Possible	2 days	Wed 25/6/18	Thu 25/6/19	Wed 25/6/18	Thu 25/6/19	Thu 25/7/3	Fri 25/7/4	15 days	0	75
77	SHT.A04~SHT.A05,1500PC,B,L=81.31,D=3.44	NA	As Possible	176 days	Fri 25/6/20	Fri 25/12/12	Fri 25/6/20	Fri 25/12/12	Sat 25/7/5	Sat 25/12/27	15 days		
78	Stage 1	NA	As Possible	60 days	Fri 25/6/20	Mon 25/8/18	Fri 25/6/20	Mon 25/8/18	Sat 25/7/5	Tue 25/9/2	15 days		
79	TTA Implementation	NA	As Possible	4 days	Fri 25/6/20	Mon 25/6/23	Fri 25/6/20	Mon 25/6/23	Sat 25/7/5	Tue 25/7/8	15 days	0	76
80	Breaking Ground	NA	As Possible	12 days	Sun 25/6/22	Thu 25/7/3	Sun 25/6/22	Thu 25/7/3	Mon 25/7/7	Fri 25/7/18	15 days	1	79FS-2 days
81	Excavation and Lateral Support	NA	As Possible	14 days	Wed 25/7/2	Tue 25/7/15	Wed 25/7/2	Tue 25/7/15	Thu 25/7/17	Wed 25/7/30	15 days	2	80FS-2 days
82	Drain Laying	NA	As Possible	12 days	Mon 25/7/14	Fri 25/7/25	Mon 25/7/14	Fri 25/7/25	Tue 25/7/29	Sat 25/8/9	15 days	2	81FS-2 days
83	Bedding and Backfilling	NA	As Possible	8 days	Thu 25/7/24	Thu 25/7/31	Thu 25/7/24	Thu 25/7/31	Fri 25/8/8	Fri 25/8/15	15 days	0	82FS-2 days
84	Manhole Construction	NA	As Possible	10 days	Wed 25/7/30	Fri 25/8/8	Wed 25/7/30	Fri 25/8/8	Thu 25/8/14	Sat 25/8/23	15 days	1	83FS-2 days
85	Reinstatement	NA	As Possible	8 days	Sat 25/8/9	Sat 25/8/16	Sat 25/8/9	Sat 25/8/16	Sun 25/8/24	Sun 25/8/31	15 days	0	84
86	TTA Removal	NA	As Possible	2 days	Sun 25/8/17	Mon 25/8/18	Sun 25/8/17	Mon 25/8/18	Mon 25/9/1	Tue 25/9/2	15 days	0	85
87	Stage 2	NA	As Possible	58 days	Tue 25/8/19	Wed 25/10/15	Tue 25/8/19	Wed 25/10/15	Wed 25/9/3	Thu 25/10/30	15 days		
88	TTA Implementation	NA	As Possible	4 days	Tue 25/8/19	Fri 25/8/22	Tue 25/8/19	Fri 25/8/22	Wed 25/9/3	Sat 25/9/6	15 days	0	86
89	Breaking Ground	NA	As Possible	10 days	Thu 25/8/21	Sat 25/8/30	Thu 25/8/21	Sat 25/8/30	Fri 25/9/5	Sun 25/9/14	15 days	1	88FS-2 days
90	Excavation and Lateral Support	NA	As Possible	14 days	Fri 25/8/29	Thu 25/9/11	Fri 25/8/29	Thu 25/9/11	Sat 25/9/13	Fri 25/9/26	15 days	2	89FS-2 days
91	Drain Laying	NA	As Possible	12 days	Wed 25/9/10	Sun 25/9/21	Wed 25/9/10	Sun 25/9/21	Thu 25/9/25	Mon 25/10/6	15 days	2	90FS-2 days
92	Bedding and Backfilling	NA	As Possible	8 days	Sat 25/9/20	Sat 25/9/27	Sat 25/9/20	Sat 25/9/27	Sun 25/10/5	Sun 25/10/12	15 days	0	91FS-2 days
93	Manhole Construction	NA	As Possible	10 days	Fri 25/9/26	Sun 25/10/5	Fri 25/9/26	Sun 25/10/5	Sat 25/10/11	Mon 25/10/20	15 days	1	92FS-2 days
94	Reinstatement	NA	As Possible	8 days	Mon 25/10/6	Mon 25/10/13	Mon 25/10/6	Mon 25/10/13	Tue 25/10/21	Tue 25/10/28	15 days	0	93
95	TTA Removal	NA	As Possible	2 days	Tue 25/10/14	Wed 25/10/15	Tue 25/10/14	Wed 25/10/15	Wed 25/10/29	Thu 25/10/30	15 days	0	94
96	Stage 3	NA	As Possible	58 days	Thu 25/10/16	Fri 25/12/12	Thu 25/10/16	Fri 25/12/12	Fri 25/10/31	Sat 25/12/27	15 days		
97	TTA Implementation	NA	As Possible	4 days	Thu 25/10/16	Sun 25/10/19	Thu 25/10/16	Sun 25/10/19	Fri 25/10/31	Mon 25/11/3	15 days	0	95,6,8
98	Breaking Ground	NA	As Possible	10 days	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	Sun 25/11/2	Tue 25/11/11	15 days	1	97FS-2 days
99	Excavation and Lateral Support	NA	As Possible	14 days	Sun 25/10/26	Sat 25/11/8	Sun 25/10/26	Sat 25/11/8	Mon 25/11/10	Sun 25/11/23	15 days	2	98FS-2 days
100	Drain Laying	NA	As Possible	12 days	Fri 25/11/7	Tue 25/11/18	Fri 25/11/7	Tue 25/11/18	Sat 25/11/22	Wed 25/12/3	15 days	2	99FS-2 days
101	Bedding and Backfilling	NA	As Possible	8 days	Mon 25/11/17	Mon 25/11/24	Mon 25/11/17	Mon 25/11/24	Tue 25/12/2	Tue 25/12/9	15 days	0	100FS-2 days
102	Manhole Construction	NA	As Possible	10 days	Sun 25/11/23	Tue 25/12/2	Sun 25/11/23	Tue 25/12/2	Mon 25/12/8	Wed 25/12/17	15 days	1	101FS-2 days
103	Reinstatement	NA	As Possible	8 days	Wed 25/12/3	Wed 25/12/10	Wed 25/12/3	Wed 25/12/10	Thu 25/12/18	Thu 25/12/25	15 days	0	102
104	TTA Removal	NA	As Possible	2 days	Thu 25/12/11	Fri 25/12/12	Thu 25/12/11	Fri 25/12/12	Fri 25/12/26	Sat 25/12/27	15 days	0	103
105	Connection of ex. 900pipe to SHT.A05	NA	As Possible	30 days	Sat 25/12/13	Sun 26/1/11	Sat 25/12/13	Sun 26/1/11	Sun 25/12/28	Mon 26/1/26	15 days	0	104
106	Connection of ex. 900pipe to SHT.A06A	NA	As Possible	30 days	Mon 26/1/12	Tue 26/2/10	Mon 26/1/12	Tue 26/2/10	Tue 26/1/27	Wed 26/2/25	15 days	0	105
107	CCTV inspection	NA	As Possible	20 days	Wed 26/2/11	Mon 26/3/2	Wed 26/2/11	Mon 26/3/2	Thu 26/2/26	Tue 26/3/17	15 days	0	106
108	Reinstatement	Mon 26/4/6	Later Than	20 days	Tue 26/3/3	Sun 26/3/22	Tue 26/3/3	Sun 26/3/22	Wed 26/3/18	Mon 26/4/6	15 days	0	107
109													
110	access date of Portion E2	########	Later Than	270 days	Tue 23/5/30	Fri 24/2/23	Tue 23/5/30	Fri 24/2/23	Fri 25/5/2	Mon 26/1/26	703 days	0	\\WingTatNasC
111	section V (Shan Ha Tsuen)	########	Later Than	973 days	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	0 days	0	\\WingTatNasC
112	Planned Completion Day	Fri 26/6/5	Later Than	130 days	Tue 26/1/27	Fri 26/6/5	Tue 26/1/27	Fri 26/6/5	Tue 26/1/27	Fri 26/6/5	0 days	0	111
113	Early Access (partial) [A]	NA	As Possible	205 days	Tue 23/5/30	Wed 23/12/20	Tue 23/5/30	Wed 23/12/20	Thu 23/8/3	Fri 24/2/23	65 days	0	\\WingTatNasC
114	Site Establishment	NA	As Possible	812 days	Tue 23/9/12	Mon 25/12/1	Tue 23/9/12	Mon 25/12/1	Tue 23/9/12	Fri 27/4/2	0 days		
115	Prepare and Accept Temp. Works Design and Method Statement [A]	NA	As Possible	798 days	Tue 23/9/26	Mon 25/12/1	Tue 23/9/26	Mon 25/12/1	Fri 24/1/12	Thu 26/3/19	108 days	0	\\WingTatNasC
116	Public Liaison and Negotiation with Village Rep.	NA	As Possible	164 days	Tue 23/9/12	Thu 24/2/22	Tue 23/9/12	Thu 24/2/22	Tue 23/9/12	Thu 24/2/22	0 days	0	\\WingTatNasC
117	[NCExxx] Objection and additional request of local landlord	NA	As Possible	40 days	Fri 24/2/23	Tue 24/4/2	Fri 24/2/23	Tue 24/4/2	Mon 27/2/22	Fri 27/4/2	1095 days		116
118	Initial Survey [A]	NA	As Possible	648 days	Fri 24/2/23	Mon 25/12/1	Fri 24/2/23	Mon 25/12/1	Mon 24/6/10	Thu 26/3/19	108 days	0	113FS-1 day,11

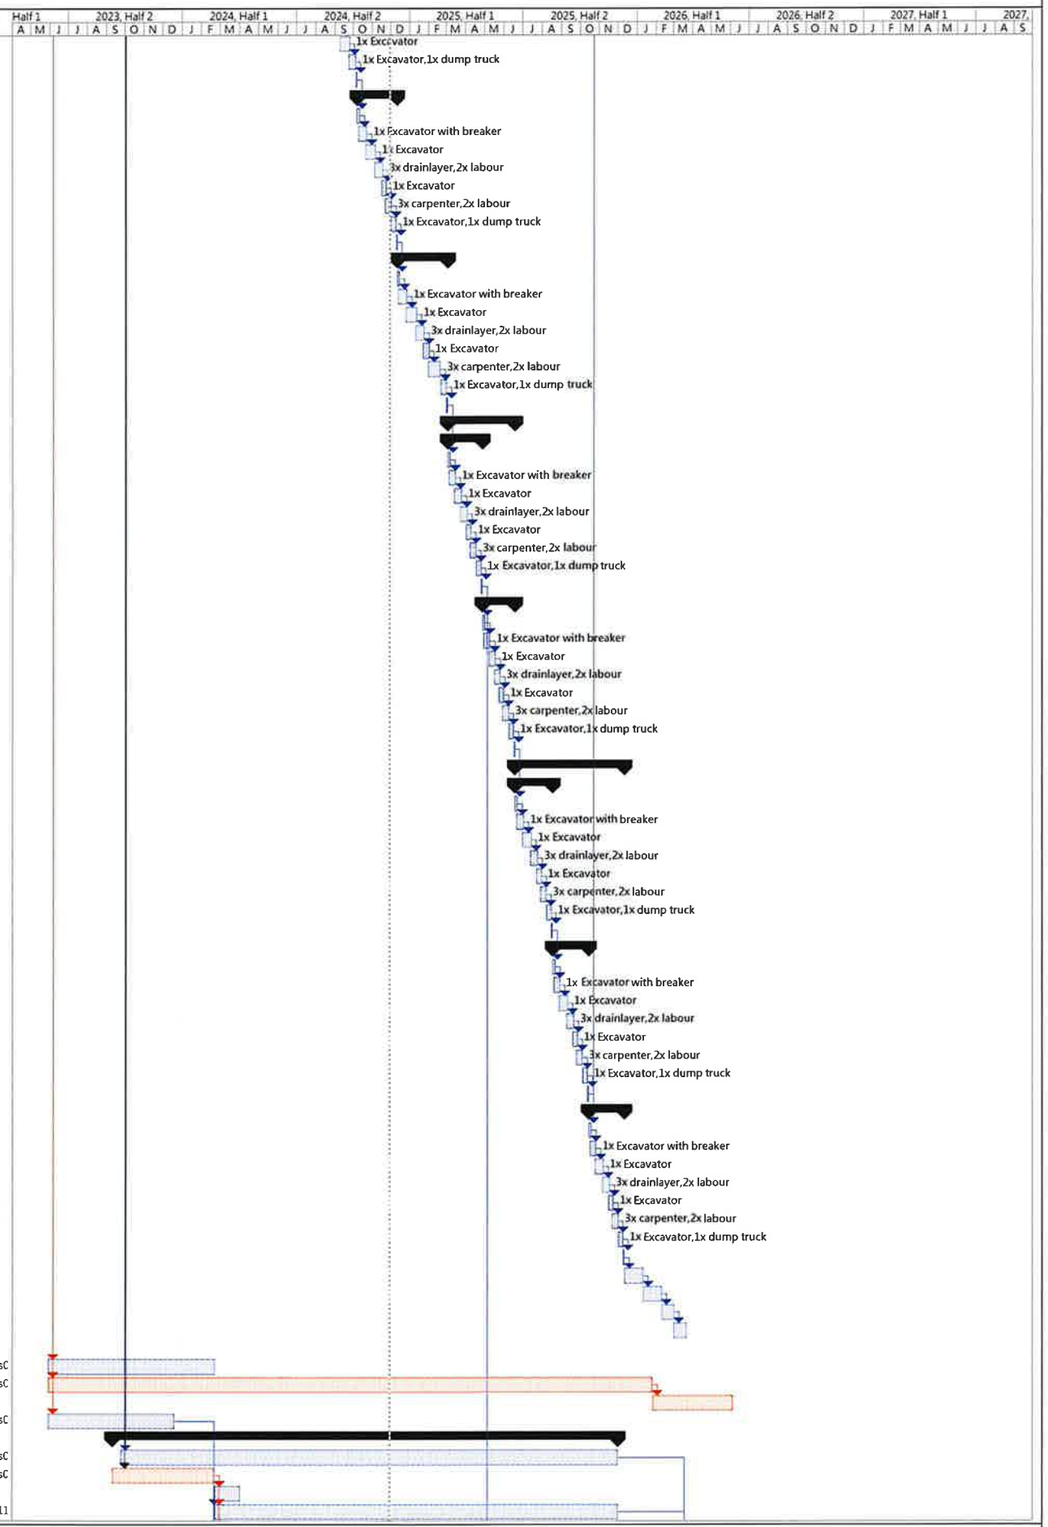


Revision.: 14.0 Date: 31 October 2024

´Task Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary
Critical Task Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline


Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
119	Initial Safety & Environmental measures [A]	NA	As Possible	21 days	Fri 24/2/23	Thu 24/3/14	Fri 24/2/23	Thu 24/3/14	Fri 24/2/23	Thu 24/3/14	0 days	0	116,113FS-1 da
120	Setup of instrumentation and monitoring [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Sat 27/3/6	Fri 27/4/2	1086 days	0	119
121	Condition Survey [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	119
122	Tree Survey [A]	NA	As Possible	28 days	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	119
123	Built Heritage Survey [A]	NA	As Possible	200 days	Fri 24/3/15	Mon 24/9/30	Fri 24/3/15	Mon 24/9/30	Tue 26/9/15	Fri 27/4/2	914 days	0	119
124	UU detection [A]	NA	As Possible	28 days	Fri 24/4/12	Thu 24/5/9	Fri 24/4/12	Thu 24/5/9	Fri 24/4/12	Thu 24/5/9	0 days	0	121,122
125	Site Clearance [A]	NA	As Possible	28 days	Fri 24/5/3	Thu 24/5/30	Fri 24/5/3	Thu 24/5/30	Fri 24/5/3	Thu 24/5/30	0 days	0	124FS-7 days
126	**Drain Laying Works (West)**	**NA**	**As Possible**	**676 days**	**Fri 24/5/31**	**Mon 26/4/6**	**Fri 24/5/31**	**Mon 26/4/6**	**Fri 24/5/31**	**Fri 26/6/5**	**0 days**		
127	**SHT.B02~SHT.B03,900PC,B,L=36.94,D=1.72**	**NA**	**As Possible**	**82 days**	**Fri 24/5/31**	**Tue 24/8/20**	**Fri 24/5/31**	**Tue 24/8/20**	**Fri 24/5/31**	**Tue 24/8/20**	**0 days**		
128	**Stage 1**	**NA**	**As Possible**	**41 days**	**Fri 24/5/31**	**Wed 24/7/10**	**Fri 24/5/31**	**Wed 24/7/10**	**Fri 24/5/31**	**Wed 24/7/10**	**0 days**		
129	TTA implementation [A]	NA	As Possible	4 days	Fri 24/5/31	Mon 24/6/3	Fri 24/5/31	Mon 24/6/3	Fri 24/5/31	Mon 24/6/3	0 days	0	125
130	Breaking pavement [A]	NA	As Possible	6 days	Sun 24/6/2	Fri 24/6/7	Sun 24/6/2	Fri 24/6/7	Sun 24/6/2	Fri 24/6/7	0 days	0	129FS-2 days
131	Excavation and Lateral Support [A]	NA	As Possible	14 days	Thu 24/6/6	Wed 24/6/19	Thu 24/6/6	Wed 24/6/19	Thu 24/6/6	Wed 24/6/19	0 days	0	130FS-2 days
132	Manhole bedding construction [A]	NA	As Possible	6 days	Tue 24/6/18	Sun 24/6/23	Tue 24/6/18	Sun 24/6/23	Tue 24/6/18	Sun 24/6/23	0 days	0	131FS-2 days
133	Drain Laying [A]	NA	As Possible	6 days	Sat 24/6/22	Thu 24/6/27	Sat 24/6/22	Thu 24/6/27	Sat 24/6/22	Thu 24/6/27	0 days	0	132FS-2 days
134	Manhole construction [A]	NA	As Possible	6 days	Wed 24/6/26	Mon 24/7/1	Wed 24/6/26	Mon 24/7/1	Wed 24/6/26	Mon 24/7/1	0 days	0	133FS-2 days
135	Backfilling and Compaction [A]	NA	As Possible	5 days	Sun 24/6/30	Thu 24/7/4	Sun 24/6/30	Thu 24/7/4	Sun 24/6/30	Thu 24/7/4	0 days	0	134FS-2 days
136	Reinstatement [A]	NA	As Possible	5 days	Fri 24/7/5	Tue 24/7/9	Fri 24/7/5	Tue 24/7/9	Fri 24/7/5	Tue 24/7/9	0 days	0	135
137	TTA removal [A]	NA	As Possible	1 day	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	0 days	0	136
138	**Stage 2**	**NA**	**As Possible**	**41 days**	**Thu 24/7/11**	**Tue 24/8/20**	**Thu 24/7/11**	**Tue 24/8/20**	**Thu 24/7/11**	**Tue 24/8/20**	**0 days**		
139	TTA implementation [A]	NA	As Possible	4 days	Thu 24/7/11	Sun 24/7/14	Thu 24/7/11	Sun 24/7/14	Thu 24/7/11	Sun 24/7/14	0 days	0	137
140	Breaking pavement [A]	NA	As Possible	6 days	Sat 24/7/13	Thu 24/7/18	Sat 24/7/13	Thu 24/7/18	Sat 24/7/13	Thu 24/7/18	0 days	0	139FS-2 days
141	Excavation and Lateral Support [A]	NA	As Possible	14 days	Wed 24/7/17	Tue 24/7/30	Wed 24/7/17	Tue 24/7/30	Wed 24/7/17	Tue 24/7/30	0 days	0	140FS-2 days
142	Manhole bedding construction [A]	NA	As Possible	6 days	Mon 24/7/29	Sat 24/8/3	Mon 24/7/29	Sat 24/8/3	Mon 24/7/29	Sat 24/8/3	0 days	0	141FS-2 days
143	Drain Laying [A]	NA	As Possible	6 days	Fri 24/8/2	Wed 24/8/7	Fri 24/8/2	Wed 24/8/7	Fri 24/8/2	Wed 24/8/7	0 days	0	142FS-2 days
144	Manhole construction [A]	NA	As Possible	6 days	Tue 24/8/6	Sun 24/8/11	Tue 24/8/6	Sun 24/8/11	Tue 24/8/6	Sun 24/8/11	0 days	0	143FS-2 days
145	Backfilling and Compaction [A]	NA	As Possible	5 days	Sat 24/8/10	Wed 24/8/14	Sat 24/8/10	Wed 24/8/14	Sat 24/8/10	Wed 24/8/14	0 days	0	144FS-2 days
146	Reinstatement	NA	As Possible	5 days	Thu 24/8/15	Mon 24/8/19	Thu 24/8/15	Mon 24/8/19	Thu 24/8/15	Mon 24/8/19	0 days	0	145
147	TTA removal	NA	As Possible	1 day	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	0 days	0	146
148	**SHT.B03~SHT.B04,900PC,B,L=21,D=1.97**	**NA**	**As Possible**	**39 days**	**Wed 24/8/21**	**Sat 24/9/28**	**Wed 24/8/21**	**Sat 24/9/28**	**Wed 24/8/21**	**Sat 24/9/28**	**0 days**		
149	TTA implementation [A]	NA	As Possible	4 days	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	0 days	0	147
150	Breaking pavement [A]	NA	As Possible	6 days	Fri 24/8/23	Wed 24/8/28	Fri 24/8/23	Wed 24/8/28	Fri 24/8/23	Wed 24/8/28	0 days	0	149FS-2 days
151	Excavation and Lateral Support [A]	NA	As Possible	12 days	Tue 24/8/27	Sat 24/9/7	Tue 24/8/27	Sat 24/9/7	Tue 24/8/27	Sat 24/9/7	0 days	0	150FS-2 days
152	Manhole bedding construction [A]	NA	As Possible	6 days	Fri 24/9/6	Wed 24/9/11	Fri 24/9/6	Wed 24/9/11	Fri 24/9/6	Wed 24/9/11	0 days	0	151FS-2 days
153	Drain Laying	NA	As Possible	6 days	Tue 24/9/10	Sun 24/9/15	Tue 24/9/10	Sun 24/9/15	Tue 24/9/10	Sun 24/9/15	0 days	0	152FS-2 days
154	Manhole construction [A]	NA	As Possible	6 days	Sat 24/9/14	Thu 24/9/19	Sat 24/9/14	Thu 24/9/19	Sat 24/9/14	Thu 24/9/19	0 days	0	153FS-2 days
155	Backfilling and Compaction [A]	NA	As Possible	5 days	Wed 24/9/18	Sun 24/9/22	Wed 24/9/18	Sun 24/9/22	Wed 24/9/18	Sun 24/9/22	0 days	0	154FS-2 days
156	Reinstatement [A]	NA	As Possible	5 days	Mon 24/9/23	Fri 24/9/27	Mon 24/9/23	Fri 24/9/27	Mon 24/9/23	Fri 24/9/27	0 days	0	155
157	TTA removal [A]	NA	As Possible	1 day	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	0 days	0	156
158	**SHT.B01~SHT.B02,900PC,B,L=61.6,D=1.59**	**NA**	**As Possible**	**134 days**	**Sun 24/9/29**	**Sun 25/2/9**	**Sun 24/9/29**	**Sun 25/2/9**	**Sun 24/9/29**	**Sun 25/2/9**	**0 days**		
159	**Stage 1**	**NA**	**As Possible**	**97 days**	**Sun 24/9/29**	**Fri 25/1/3**	**Sun 24/9/29**	**Fri 25/1/3**	**Sun 24/9/29**	**Fri 25/1/3**	**0 days**		
160	TTA implementation [A]	NA	As Possible	4 days	Sun 24/9/29	Wed 24/10/2	Sun 24/9/29	Wed 24/10/2	Sun 24/9/29	Wed 24/10/2	0 days	0	157
161	Breaking pavement [A]	NA	As Possible	6 days	Tue 24/10/1	Sun 24/10/6	Tue 24/10/1	Sun 24/10/6	Tue 24/10/1	Sun 24/10/6	0 days	0	160FS-2 days
162	[NCExxx] CLP cable diversion	NA	As Possible	60 days	Sat 24/10/5	Tue 24/12/3	Sat 24/10/5	Tue 24/12/3	Sat 24/10/5	Tue 24/12/3	0 days	0	161FS-2 days
163	Excavation and Lateral Support	NA	As Possible	10 days	Wed 24/12/4	Fri 24/12/13	Wed 24/12/4	Fri 24/12/13	Wed 24/12/4	Fri 24/12/13	0 days	0	162
164	Manhole bedding construction	NA	As Possible	6 days	Thu 24/12/12	Tue 24/12/17	Thu 24/12/12	Tue 24/12/17	Thu 24/12/12	Tue 24/12/17	0 days	0	163FS-2 days
165	Drain Laying	NA	As Possible	6 days	Mon 24/12/16	Sat 24/12/21	Mon 24/12/16	Sat 24/12/21	Mon 24/12/16	Sat 24/12/21	0 days	0	164FS-2 days
166	Manhole construction	NA	As Possible	6 days	Fri 24/12/20	Wed 24/12/25	Fri 24/12/20	Wed 24/12/25	Fri 24/12/20	Wed 24/12/25	0 days	0	165FS-2 days
167	Backfilling and Compaction	NA	As Possible	5 days	Tue 24/12/24	Sat 24/12/28	Tue 24/12/24	Sat 24/12/28	Tue 24/12/24	Sat 24/12/28	0 days	0	166FS-2 days
168	Reinstatement	NA	As Possible	5 days	Sun 24/12/29	Thu 25/1/2	Sun 24/12/29	Thu 25/1/2	Sun 24/12/29	Thu 25/1/2	0 days	0	167
169	TTA removal	NA	As Possible	1 day	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	0 days	0	168
170	**Stage 2**	**NA**	**As Possible**	**37 days**	**Sat 25/1/4**	**Sun 25/2/9**	**Sat 25/1/4**	**Sun 25/2/9**	**Sat 25/1/4**	**Sun 25/2/9**	**0 days**		
171	TTA implementation	NA	As Possible	4 days	Sat 25/1/4	Tue 25/1/7	Sat 25/1/4	Tue 25/1/7	Sat 25/1/4	Tue 25/1/7	0 days	0	169
172	Breaking pavement	NA	As Possible	6 days	Mon 25/1/6	Sat 25/1/11	Mon 25/1/6	Sat 25/1/11	Mon 25/1/6	Sat 25/1/11	0 days	0	171FS-2 days
173	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/1/10	Sun 25/1/19	Fri 25/1/10	Sun 25/1/19	Fri 25/1/10	Sun 25/1/19	0 days	0	172FS-2 days
174	Manhole bedding construction	NA	As Possible	6 days	Sat 25/1/18	Thu 25/1/23	Sat 25/1/18	Thu 25/1/23	Sat 25/1/18	Thu 25/1/23	0 days	0	173FS-2 days
175	Drain Laying	NA	As Possible	6 days	Wed 25/1/22	Mon 25/1/27	Wed 25/1/22	Mon 25/1/27	Wed 25/1/22	Mon 25/1/27	0 days	0	174FS-2 days
176	Manhole construction	NA	As Possible	6 days	Sun 25/1/26	Fri 25/1/31	Sun 25/1/26	Fri 25/1/31	Sun 25/1/26	Fri 25/1/31	0 days	0	175FS-2 days
177	Backfilling and Compaction	NA	As Possible	5 days	Thu 25/1/30	Mon 25/2/3	Thu 25/1/30	Mon 25/2/3	Thu 25/1/30	Mon 25/2/3	0 days	0	176FS-2 days
178	Reinstatement	NA	As Possible	5 days	Tue 25/2/4	Sat 25/2/8	Tue 25/2/4	Sat 25/2/8	Tue 25/2/4	Sat 25/2/8	0 days	0	177
179	TTA removal	NA	As Possible	1 day	Sun 25/2/9	Sun 25/2/9	Sun 25/2/9	Sun 25/2/9	Sun 25/2/9	Sun 25/2/9	0 days	0	178
180	**SHT.CP2~SHT.B01,900PC,B,L=10.36,D=1.59**	**NA**	**As Possible**	**37 days**	**Mon 25/2/10**	**Tue 25/3/18**	**Mon 25/2/10**	**Tue 25/3/18**	**Mon 25/2/10**	**Tue 25/3/18**	**0 days**		
181	TTA implementation	NA	As Possible	3 days	Mon 25/2/10	Wed 25/2/12	Mon 25/2/10	Wed 25/2/12	Mon 25/2/10	Wed 25/2/12	0 days	0	179
182	Breaking pavement	NA	As Possible	6 days	Tue 25/2/11	Sun 25/2/16	Tue 25/2/11	Sun 25/2/16	Tue 25/2/11	Sun 25/2/16	0 days	0	181FS-2 days
183	Excavation and Lateral Support	NA	As Possible	10 days	Sat 25/2/15	Mon 25/2/24	Sat 25/2/15	Mon 25/2/24	Sat 25/2/15	Mon 25/2/24	0 days	0	182FS-2 days
184	Manhole bedding construction	NA	As Possible	6 days	Sun 25/2/23	Fri 25/2/28	Sun 25/2/23	Fri 25/2/28	Sun 25/2/23	Fri 25/2/28	0 days	0	183FS-2 days
185	Drain Laying	NA	As Possible	6 days	Thu 25/2/27	Tue 25/3/4	Thu 25/2/27	Tue 25/3/4	Thu 25/2/27	Tue 25/3/4	0 days	0	184FS-2 days
186	Manhole construction	NA	As Possible	7 days	Mon 25/3/3	Sun 25/3/9	Mon 25/3/3	Sun 25/3/9	Mon 25/3/3	Sun 25/3/9	0 days	0	185FS-2 days
187	Backfilling and Compaction	NA	As Possible	5 days	Sat 25/3/8	Wed 25/3/12	Sat 25/3/8	Wed 25/3/12	Sat 25/3/8	Wed 25/3/12	0 days	0	186FS-2 days
188	Reinstatement	NA	As Possible	5 days	Thu 25/3/13	Mon 25/3/17	Thu 25/3/13	Mon 25/3/17	Thu 25/3/13	Mon 25/3/17	0 days	0	187
189	TTA removal	NA	As Possible	1 day	Tue 25/3/18	Tue 25/3/18	Tue 25/3/18	Tue 25/3/18	Tue 25/3/18	Tue 25/3/18	0 days	0	188
190	**SHT.B04~SHT.A1A,900PC,B,L=13.155D=2.06**	**NA**	**As Possible**	**54 days**	**Tue 25/4/15**	**Sat 25/6/7**	**Tue 25/4/15**	**Sat 25/6/7**	**Sat 25/6/14**	**Wed 25/8/6**	**60 days**		
191	TTA implementation	NA	As Possible	3 days	Tue 25/4/15	Thu 25/4/17	Tue 25/4/15	Thu 25/4/17	Sat 25/6/14	Mon 25/6/16	60 days	0	67FS-14 days
192	Breaking pavement	NA	As Possible	6 days	Wed 25/4/16	Mon 25/4/21	Wed 25/4/16	Mon 25/4/21	Sun 25/6/15	Fri 25/6/20	60 days	0	191FS-2 days
193	Excavation and Lateral Support	NA	As Possible	14 days	Sun 25/4/20	Sat 25/5/3	Sun 25/4/20	Sat 25/5/3	Thu 25/6/19	Wed 25/7/2	60 days	0	192FS-2 days
194	Manhole bedding construction	NA	As Possible	10 days	Fri 25/5/2	Sun 25/5/11	Fri 25/5/2	Sun 25/5/11	Tue 25/7/1	Thu 25/7/10	60 days	0	193FS-2 days
195	Drain Laying	NA	As Possible	10 days	Sat 25/5/10	Mon 25/5/19	Sat 25/5/10	Mon 25/5/19	Wed 25/7/9	Fri 25/7/18	60 days	0	194FS-2 days
196	Manhole construction	NA	As Possible	10 days	Sun 25/5/18	Tue 25/5/27	Sun 25/5/18	Tue 25/5/27	Thu 25/7/17	Sat 25/7/26	60 days	0	195FS-2 days
197	Backfilling and Compaction	NA	As Possible	6 days	Mon 25/5/26	Sat 25/5/31	Mon 25/5/26	Sat 25/5/31	Fri 25/7/25	Wed 25/7/30	60 days	0	196FS-2 days
198	Reinstatement	NA	As Possible	6 days	Sun 25/6/1	Fri 25/6/6	Sun 25/6/1	Fri 25/6/6	Thu 25/7/31	Tue 25/8/5	60 days	0	197
199	TTA removal	NA	As Possible	1 day	Sat 25/6/7	Sat 25/6/7	Sat 25/6/7	Sat 25/6/7	Wed 25/8/6	Wed 25/8/6	60 days	0	198
200	Connection of ex. UC to SHT.A1A	Fri 26/6/5	o Later Than	28 days	Sun 25/6/8	Sat 25/7/5	Sun 25/6/8	Sat 25/7/5	Thu 25/8/7	Wed 25/9/3	60 days	0	199

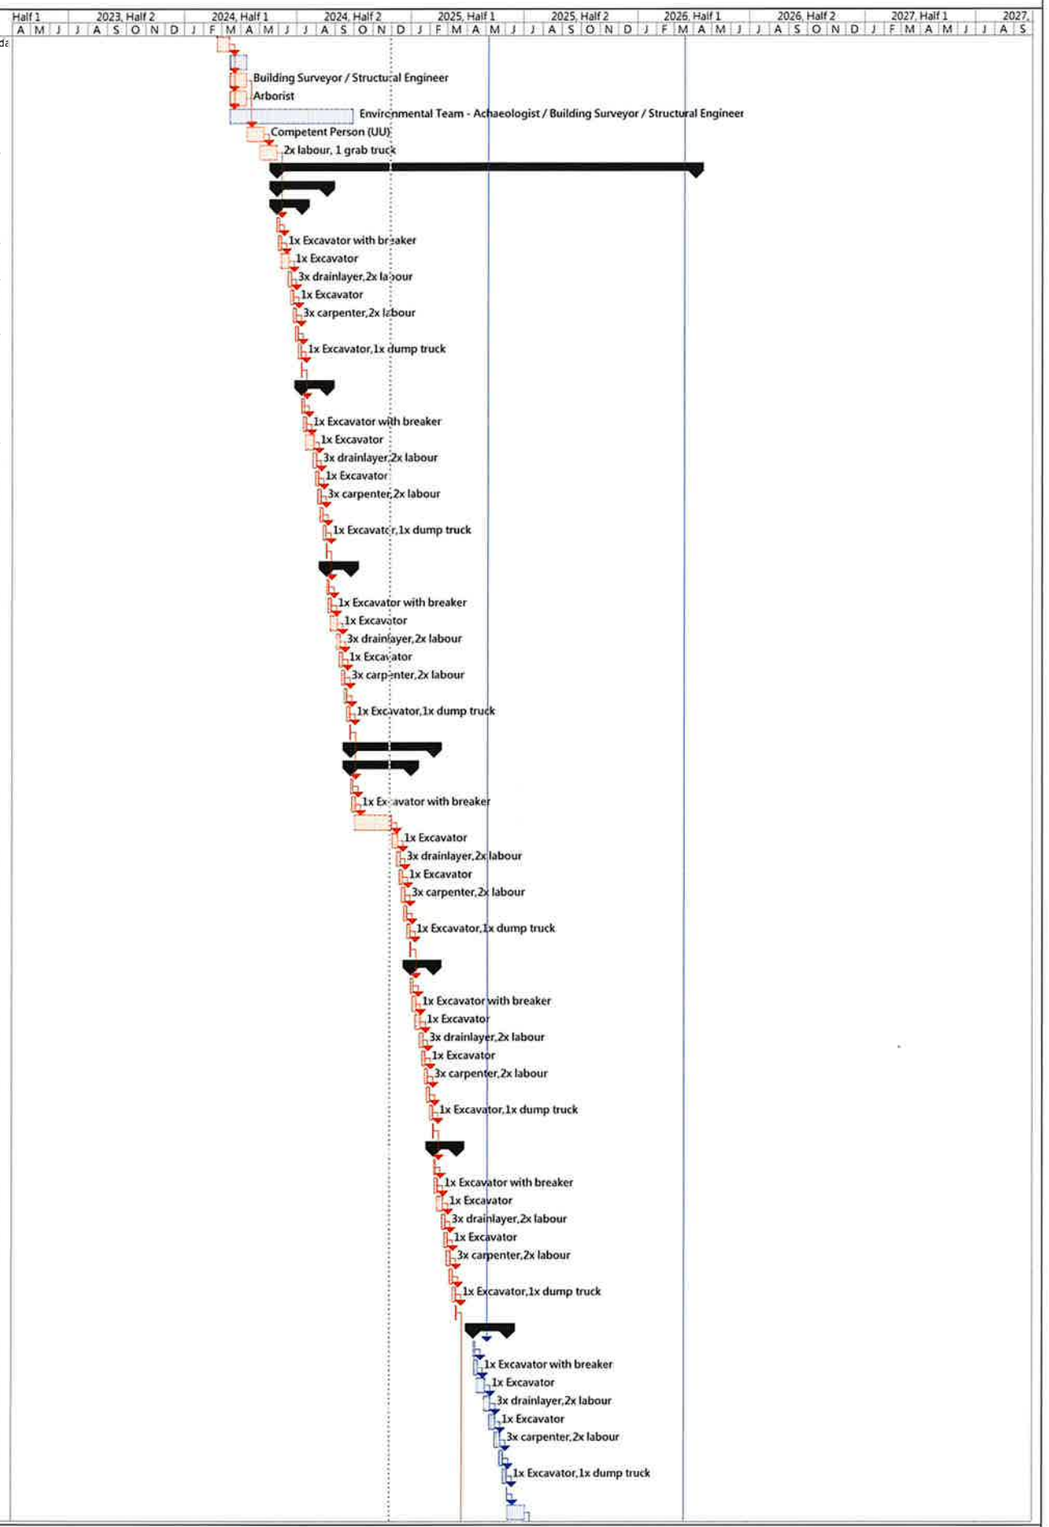

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
201	**SHT.CP1~SHT.A1A,550PC,B,L=4.16,D=2.06**	**NA**	**As Possible**	**53 days**	**Sun 25/7/6**	**Wed 25/8/27**	**Sun 25/7/6**	**Wed 25/8/27**	**Thu 25/9/4**	**Sun 25/10/26**	**60 days**		
202	TTA implementation	NA	As Possible	3 days	Sun 25/7/6	Tue 25/7/8	Sun 25/7/6	Tue 25/7/8	Thu 25/9/4	Sat 25/9/6	60 days	0	200
203	Breaking pavement	NA	As Possible	7 days	Mon 25/7/7	Sun 25/7/13	Mon 25/7/7	Sun 25/7/13	Fri 25/9/5	Thu 25/9/11	60 days	0	202FS-2 days
204	Excavation and Lateral Support	NA	As Possible	12 days	Sat 25/7/12	Wed 25/7/23	Sat 25/7/12	Wed 25/7/23	Wed 25/9/10	Sun 25/9/21	60 days	0	203FS-2 days
205	Manhole bedding construction	NA	As Possible	10 days	Tue 25/7/22	Thu 25/7/31	Tue 25/7/22	Thu 25/7/31	Sat 25/9/20	Mon 25/9/29	60 days	0	204FS-2 days
206	Drain Laying	NA	As Possible	10 days	Wed 25/7/30	Fri 25/8/8	Wed 25/7/30	Fri 25/8/8	Sun 25/9/28	Tue 25/10/7	60 days	0	205FS-2 days
207	Manhole construction	NA	As Possible	10 days	Thu 25/8/7	Sat 25/8/16	Thu 25/8/7	Sat 25/8/16	Mon 25/10/6	Wed 25/10/15	60 days	0	206FS-2 days
208	Backfilling and Compaction	NA	As Possible	6 days	Fri 25/8/15	Wed 25/8/20	Fri 25/8/15	Wed 25/8/20	Tue 25/10/14	Sun 25/10/19	60 days	0	207FS-2 days
209	Reinstatement	NA	As Possible	6 days	Thu 25/8/21	Tue 25/8/26	Thu 25/8/21	Tue 25/8/26	Mon 25/10/20	Sat 25/10/25	60 days	0	208
210	TTA removal	NA	As Possible	1 day	Wed 25/8/27	Wed 25/8/27	Wed 25/8/27	Wed 25/8/27	Sun 25/10/26	Sun 25/10/26	60 days	0	209
211	Connection of ex. 550pipe to SHT.CP1	Fri 26/6/5	Later Than	28 days	Thu 25/8/28	Wed 25/9/24	Thu 25/8/28	Wed 25/9/24	Mon 25/10/27	Sun 25/11/23	60 days	0	210
212	**SHT.A1A~SHT.A01,1200PC,B,L=7.675,D=2.14**	**NA**	**As Possible**	**47 days**	**Thu 25/9/25**	**Mon 25/11/10**	**Thu 25/9/25**	**Mon 25/11/10**	##########	**Fri 26/1/9**	**60 days**		
213	TTA implementation	NA	As Possible	4 days	Thu 25/9/25	Sun 25/9/28	Thu 25/9/25	Sun 25/9/28	Mon 25/11/24	Thu 25/11/27	60 days	0	211
214	Breaking pavement	NA	As Possible	6 days	Sat 25/9/27	Thu 25/10/2	Sat 25/9/27	Thu 25/10/2	Wed 25/11/26	Mon 25/12/1	60 days	0	213FS-2 days
215	Excavation and Lateral Support	NA	As Possible	12 days	Wed 25/10/1	Sun 25/10/12	Wed 25/10/1	Sun 25/10/12	Sun 25/11/30	Thu 25/12/11	60 days	0	214FS-2 days
216	Manhole bedding construction	NA	As Possible	8 days	Sat 25/10/11	Sat 25/10/18	Sat 25/10/11	Sat 25/10/18	Wed 25/12/10	Wed 25/12/17	60 days	0	215FS-2 days
217	Drain Laying	NA	As Possible	8 days	Fri 25/10/17	Fri 25/10/24	Fri 25/10/17	Fri 25/10/24	Tue 25/12/16	Tue 25/12/23	60 days	0	216FS-2 days
218	Manhole construction	NA	As Possible	8 days	Thu 25/10/23	Thu 25/10/30	Thu 25/10/23	Thu 25/10/30	Mon 25/12/22	Mon 25/12/29	60 days	0	217FS-2 days
219	Backfilling and Compaction	NA	As Possible	6 days	Wed 25/10/29	Mon 25/11/3	Wed 25/10/29	Mon 25/11/3	Sun 25/12/28	Fri 26/1/2	60 days	0	218FS-2 days
220	Reinstatement	NA	As Possible	6 days	Tue 25/11/4	Sun 25/11/9	Tue 25/11/4	Sun 25/11/9	Sat 26/1/3	Thu 26/1/8	60 days	0	219
221	TTA removal	NA	As Possible	1 day	Mon 25/11/10	Mon 25/11/10	Mon 25/11/10	Mon 25/11/10	Fri 26/1/9	Fri 26/1/9	60 days	0	220
222	Connection of ex. Pipe to SHT.A01	Fri 26/6/5	Later Than	28 days	Tue 25/11/11	Mon 25/12/8	Tue 25/11/11	Mon 25/12/8	Sat 26/1/10	Fri 26/2/6	60 days	0	221
223	**SHT.A01~SHT.A02,1500PC,B,L=8.39,D=3.6**	**NA**	**As Possible**	**42 days**	**Tue 25/12/9**	**Mon 26/1/19**	**Tue 25/12/9**	**Mon 26/1/19**	**Sat 26/2/7**	**Fri 26/3/20**	**60 days**		
224	TTA implementation	NA	As Possible	4 days	Tue 25/12/9	Fri 25/12/12	Tue 25/12/9	Fri 25/12/12	Sat 26/2/7	Tue 26/2/10	60 days	0	222
225	Breaking pavement	NA	As Possible	5 days	Thu 25/12/11	Mon 25/12/15	Thu 25/12/11	Mon 25/12/15	Mon 26/2/9	Fri 26/2/13	60 days	0	224FS-2 days
226	Excavation and Lateral Support	NA	As Possible	12 days	Sun 25/12/14	Thu 25/12/25	Sun 25/12/14	Thu 25/12/25	Thu 26/2/12	Mon 26/2/23	60 days	0	225FS-2 days
227	Drain Laying	NA	As Possible	6 days	Wed 25/12/24	Mon 25/12/29	Wed 25/12/24	Mon 25/12/29	Sun 26/2/22	Fri 26/2/27	60 days	0	226FS-2 days
228	Bedding and Backfilling	NA	As Possible	6 days	Sun 25/12/28	Fri 26/1/2	Sun 25/12/28	Fri 26/1/2	Thu 26/2/26	Tue 26/3/3	60 days	0	227FS-2 days
229	Manhole construction	NA	As Possible	8 days	Thu 26/1/1	Thu 26/1/8	Thu 26/1/1	Thu 26/1/8	Mon 26/3/2	Mon 26/3/9	60 days	0	228FS-2 days
230	Backfilling and Compaction	NA	As Possible	6 days	Wed 26/1/7	Mon 26/1/12	Wed 26/1/7	Mon 26/1/12	Sun 26/3/8	Fri 26/3/13	60 days	0	229FS-2 days
231	Reinstatement	NA	As Possible	6 days	Tue 26/1/13	Sun 26/1/18	Tue 26/1/13	Sun 26/1/18	Sat 26/3/14	Thu 26/3/19	60 days	0	230
232	TTA removal	NA	As Possible	1 day	Mon 26/1/19	Mon 26/1/19	Mon 26/1/19	Mon 26/1/19	Fri 26/3/20	Fri 26/3/20	60 days	0	231
233	Temporary decking over ex. UC	NA	As Possible	28 days	Tue 26/1/20	Mon 26/2/16	Tue 26/1/20	Mon 26/2/16	Sat 26/3/21	Fri 26/4/17	60 days	0	232
234	CCTV inspection	NA	As Possible	28 days	Tue 26/2/3	Mon 26/3/2	Tue 26/2/3	Mon 26/3/2	Sat 26/4/4	Fri 26/5/1	60 days	0	233FS-14 days
235	Reinstatement	Fri 26/6/5	Later Than	35 days	Tue 26/3/3	Mon 26/4/6	Tue 26/3/3	Mon 26/4/6	Sat 26/5/2	Fri 26/6/5	60 days	0	234
236	**U-Channel Works (West)**	**NA**	**As Possible**	**445 days**	**Wed 25/3/19**	**Sat 26/6/6**	**Wed 25/3/19**	**Sat 26/6/6**	**Wed 25/3/19**	**Fri 27/4/2**	**0 days**		
237	**End~ex. UC,450CU(G),L=70**	**NA**	**As Possible**	**111 days**	**Wed 25/3/19**	**Mon 25/7/7**	**Wed 25/3/19**	**Mon 25/7/7**	**Wed 25/3/19**	**Mon 25/7/7**	**0 days**		
238	**Stage 1**	**NA**	**As Possible**	**29 days**	**Wed 25/3/19**	**Wed 25/4/16**	**Wed 25/3/19**	**Wed 25/4/16**	**Wed 25/3/19**	**Wed 25/4/16**	**0 days**		
239	Excavation and Lateral Support [A]	NA	As Possible	10 days	Wed 25/3/19	Fri 25/3/28	Wed 25/3/19	Fri 25/3/28	Wed 25/3/19	Fri 25/3/28	0 days	0	189
240	Formwork Erection [A]	NA	As Possible	12 days	Thu 25/3/27	Mon 25/4/7	Thu 25/3/27	Mon 25/4/7	Thu 25/3/27	Mon 25/4/7	0 days	0	239FS-2 days
241	Catchpit construcion [A]	NA	As Possible	11 days	Sun 25/4/6	Wed 25/4/16	Sun 25/4/6	Wed 25/4/16	Sun 25/4/6	Wed 25/4/16	0 days	0	240FS-2 days
242	Concreting [A]	NA	As Possible	1 day	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	Tue 25/4/15	0 days	0	241FS-2 days
243	**Stage 2**	**NA**	**As Possible**	**29 days**	**Wed 25/4/16**	**Wed 25/5/14**	**Wed 25/4/16**	**Wed 25/5/14**	**Wed 25/4/16**	**Wed 25/5/14**	**0 days**		
244	Excavation and Lateral Support [A]	NA	As Possible	10 days	Wed 25/4/16	Fri 25/4/25	Wed 25/4/16	Fri 25/4/25	Wed 25/4/16	Fri 25/4/25	0 days	0	242
245	Formwork Erection [A]	NA	As Possible	12 days	Thu 25/4/24	Mon 25/5/5	Thu 25/4/24	Mon 25/5/5	Thu 25/4/24	Mon 25/5/5	0 days	0	244FS-2 days
246	Catchpit construcion [A]	NA	As Possible	11 days	Sun 25/5/4	Wed 25/5/14	Sun 25/5/4	Wed 25/5/14	Sun 25/5/4	Wed 25/5/14	0 days	0	245FS-2 days
247	Concreting [A]	NA	As Possible	1 day	Tue 25/5/13	Tue 25/5/13	Tue 25/5/13	Tue 25/5/13	Tue 25/5/13	Tue 25/5/13	0 days	0	246FS-2 days
248	**Stage 3**	**NA**	**As Possible**	**29 days**	**Wed 25/5/14**	**Wed 25/6/11**	**Wed 25/5/14**	**Wed 25/6/11**	**Wed 25/5/14**	**Wed 25/6/11**	**0 days**		
249	Excavation and Lateral Support [A]	NA	As Possible	10 days	Wed 25/5/14	Fri 25/5/23	Wed 25/5/14	Fri 25/5/23	Wed 25/5/14	Fri 25/5/23	0 days	0	247
250	Formwork Erection [A]	NA	As Possible	12 days	Thu 25/5/22	Mon 25/6/2	Thu 25/5/22	Mon 25/6/2	Thu 25/5/22	Mon 25/6/2	0 days	0	249FS-2 days
251	Catchpit construcion	NA	As Possible	11 days	Sun 25/6/1	Wed 25/6/11	Sun 25/6/1	Wed 25/6/11	Sun 25/6/1	Wed 25/6/11	0 days	0	250FS-2 days
252	Concreting	NA	As Possible	1 day	Tue 25/6/10	Tue 25/6/10	Tue 25/6/10	Tue 25/6/10	Tue 25/6/10	Tue 25/6/10	0 days	0	251FS-2 days
253	**Stage 4**	**NA**	**As Possible**	**27 days**	**Wed 25/6/11**	**Mon 25/7/7**	**Wed 25/6/11**	**Mon 25/7/7**	**Wed 25/6/11**	**Mon 25/7/7**	**0 days**		
254	Excavation and Lateral Support	NA	As Possible	10 days	Wed 25/6/11	Fri 25/6/20	Wed 25/6/11	Fri 25/6/20	Wed 25/6/11	Fri 25/6/20	0 days	0	252
255	Formwork Erection [A]	NA	As Possible	11 days	Thu 25/6/19	Sun 25/6/29	Thu 25/6/19	Sun 25/6/29	Thu 25/6/19	Sun 25/6/29	0 days	0	254FS-2 days
256	Catchpit construcion	NA	As Possible	10 days	Sat 25/6/28	Mon 25/7/7	Sat 25/6/28	Mon 25/7/7	Sat 25/6/28	Mon 25/7/7	0 days	0	255FS-2 days
257	Concreting	Fri 26/6/5	Later Than	1 day	Mon 25/7/7	Mon 25/7/7	Mon 25/7/7	Mon 25/7/7	Mon 25/7/7	Mon 25/7/7	0 days	0	256FS-1 day
258	**SHT.CP2.5~SHT.CP2,300->900CU(G),L=11.4**	**NA**	**As Possible**	**22 days**	**Tue 25/7/8**	**Tue 25/7/29**	**Tue 25/7/8**	**Tue 25/7/29**	**Tue 25/7/8**	**Tue 25/7/29**	**0 days**		
259	Excavation and Lateral Support [A]	NA	As Possible	6 days	Tue 25/7/8	Sun 25/7/13	Tue 25/7/8	Sun 25/7/13	Tue 25/7/8	Sun 25/7/13	0 days	0	257
260	Formwork Erection	NA	As Possible	11 days	Sat 25/7/12	Tue 25/7/22	Sat 25/7/12	Tue 25/7/22	Sat 25/7/12	Tue 25/7/22	0 days	0	259FS-2 days
261	Catchpit construcion	NA	As Possible	9 days	Mon 25/7/21	Tue 25/7/29	Mon 25/7/21	Tue 25/7/29	Mon 25/7/21	Tue 25/7/29	0 days	0	260FS-2 days
262	Concreting	NA	As Possible	1 day	Mon 25/7/28	Mon 25/7/28	Mon 25/7/28	Mon 25/7/28	Mon 25/7/28	Mon 25/7/28	0 days	0	261FS-2 days
263	**SHT.CP3~SHT.CP2.5,300->900CU(G),L=66.5**	**NA**	**As Possible**	**70 days**	**Tue 25/7/29**	**Mon 25/10/6**	**Tue 25/7/29**	**Mon 25/10/6**	**Tue 25/7/29**	**Mon 25/10/6**	**0 days**		
264	**Stage 1**	**NA**	**As Possible**	**24 days**	**Tue 25/7/29**	**Thu 25/8/21**	**Tue 25/7/29**	**Thu 25/8/21**	**Tue 25/7/29**	**Thu 25/8/21**	**0 days**		
265	Excavation and Lateral Support	NA	As Possible	8 days	Tue 25/7/29	Tue 25/8/5	Tue 25/7/29	Tue 25/8/5	Tue 25/7/29	Tue 25/8/5	0 days	0	262
266	Formwork Erection	NA	As Possible	10 days	Mon 25/8/4	Wed 25/8/13	Mon 25/8/4	Wed 25/8/13	Mon 25/8/4	Wed 25/8/13	0 days	0	265FS-2 days
267	Catchpit construcion	NA	As Possible	10 days	Tue 25/8/12	Thu 25/8/21	Tue 25/8/12	Thu 25/8/21	Tue 25/8/12	Thu 25/8/21	0 days	0	266FS-2 days
268	Concreting	NA	As Possible	1 day	Wed 25/8/20	Wed 25/8/20	Wed 25/8/20	Wed 25/8/20	Wed 25/8/20	Wed 25/8/20	0 days	0	267FS-2 days
269	**Stage 2**	**NA**	**As Possible**	**24 days**	**Thu 25/8/21**	**Sat 25/9/13**	**Thu 25/8/21**	**Sat 25/9/13**	**Thu 25/8/21**	**Sat 25/9/13**	**0 days**		
270	Excavation and Lateral Support	NA	As Possible	8 days	Thu 25/8/21	Thu 25/8/28	Thu 25/8/21	Thu 25/8/28	Thu 25/8/21	Thu 25/8/28	0 days	0	268
271	Formwork Erection	NA	As Possible	10 days	Wed 25/8/27	Fri 25/9/5	Wed 25/8/27	Fri 25/9/5	Wed 25/8/27	Fri 25/9/5	0 days	0	270FS-2 days
272	Catchpit construcion	NA	As Possible	10 days	Thu 25/9/4	Sat 25/9/13	Thu 25/9/4	Sat 25/9/13	Thu 25/9/4	Sat 25/9/13	0 days	0	271FS-2 days
273	Concreting	NA	As Possible	1 day	Fri 25/9/12	Fri 25/9/12	Fri 25/9/12	Fri 25/9/12	Fri 25/9/12	Fri 25/9/12	0 days	0	272FS-2 days
274	**Stage 3**	**NA**	**As Possible**	**24 days**	**Sat 25/9/13**	**Mon 25/10/6**	**Sat 25/9/13**	**Mon 25/10/6**	**Sat 25/9/13**	**Mon 25/10/6**	**0 days**		
275	Excavation and Lateral Support	NA	As Possible	8 days	Sat 25/9/13	Sat 25/9/20	Sat 25/9/13	Sat 25/9/20	Sat 25/9/13	Sat 25/9/20	0 days	0	273
276	Formwork Erection	NA	As Possible	10 days	Fri 25/9/19	Sun 25/9/28	Fri 25/9/19	Sun 25/9/28	Fri 25/9/19	Sun 25/9/28	0 days	0	275FS-2 days
277	Catchpit construcion	NA	As Possible	10 days	Sat 25/9/27	Mon 25/10/6	Sat 25/9/27	Mon 25/10/6	Sat 25/9/27	Mon 25/10/6	0 days	0	276FS-2 days
278	Concreting	NA	As Possible	1 day	Sun 25/10/5	Sun 25/10/5	Sun 25/10/5	Sun 25/10/5	Sun 25/10/5	Sun 25/10/5	0 days	0	277FS-2 days
279	**SHT.CP3.3~SHT.CP3,300->450CU(G),L=54.5**	**NA**	**As Possible**	**76 days**	**Mon 25/10/6**	**Sat 25/12/20**	**Mon 25/10/6**	**Sat 25/12/20**	**Mon 25/10/6**	**Sat 25/12/20**	**0 days**		
280	**Stage 1**	**NA**	**As Possible**	**24 days**	**Mon 25/10/6**	**Wed 25/10/29**	**Mon 25/10/6**	**Wed 25/10/29**	**Mon 25/10/6**	**Wed 25/10/29**	**0 days**		
281	Excavation and Lateral Support	NA	As Possible	8 days	Mon 25/10/6	Mon 25/10/13	Mon 25/10/6	Mon 25/10/13	Mon 25/10/6	Mon 25/10/13	0 days	0	278
282	Formwork Erection	NA	As Possible	10 days	Sun 25/10/12	Tue 25/10/21	Sun 25/10/12	Tue 25/10/21	Sun 25/10/12	Tue 25/10/21	0 days	0	281FS-2 days

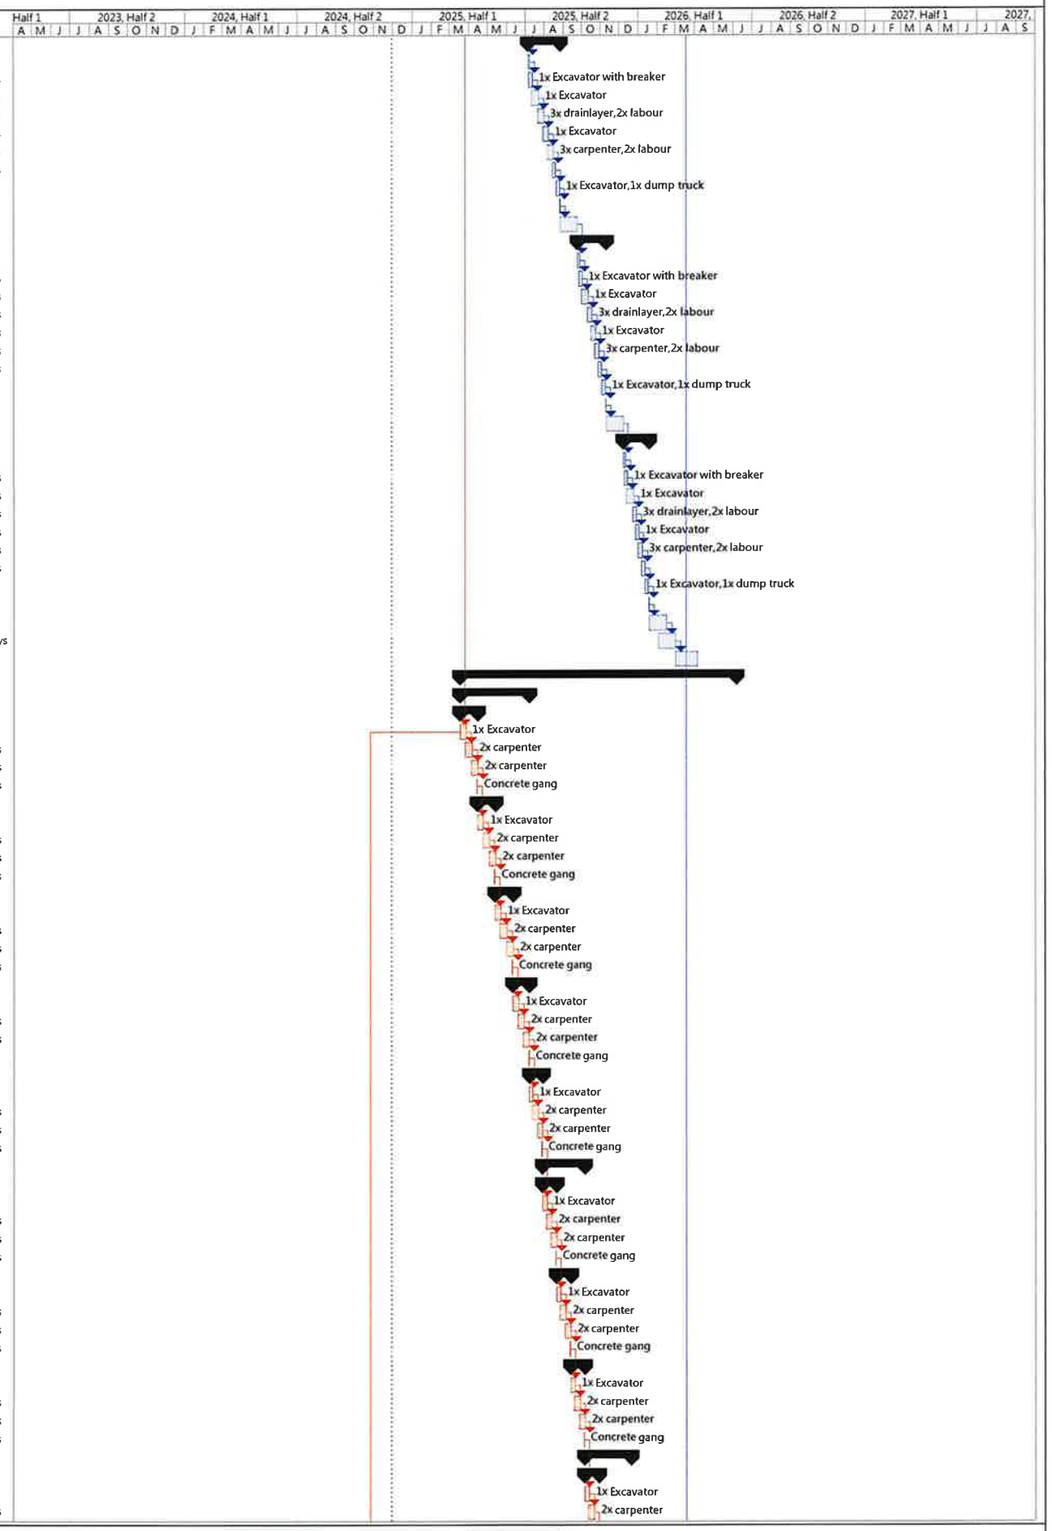


Revision.: 14.0 Date: 31 October 2024

´Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

WING TAT CIVIL ENGINEERING CO LTD
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2
PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
283	Catchpit construcion	NA	As Possible	10 days	Mon 25/10/20	Wed 25/10/29	Mon 25/10/20	Wed 25/10/29	Mon 25/10/20	Wed 25/10/29	0 days	0	282FS-2 days
284	Concreting	NA	As Possible	1 day	Tue 25/10/28	Tue 25/10/28	Tue 25/10/28	Tue 25/10/28	Tue 25/10/28	Tue 25/10/28	0 days	0	283FS-2 days
285	**Stage 2**	**NA**	**As Possible**	**27 days**	**Wed 25/10/29**	**Mon 25/11/24**	**Wed 25/10/29**	**Mon 25/11/24**	**Wed 25/10/29**	**###########**	**0 days**		
286	Excavation and Lateral Support	NA	As Possible	8 days	Wed 25/10/29	Wed 25/11/5	Wed 25/10/29	Wed 25/11/5	Wed 25/10/29	Wed 25/11/5	0 days	0	284
287	Formwork Erection	NA	As Possible	12 days	Tue 25/11/4	Sat 25/11/15	Tue 25/11/4	Sat 25/11/15	Tue 25/11/4	Sat 25/11/15	0 days	0	286FS-2 days
288	Catchpit construcion	NA	As Possible	11 days	Fri 25/11/14	Mon 25/11/24	Fri 25/11/14	Mon 25/11/24	Fri 25/11/14	Mon 25/11/24	0 days	0	287FS-2 days
289	Concreting	NA	As Possible	1 day	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	0 days	0	288FS-2 days
290	**Stage 3**	**NA**	**As Possible**	**27 days**	**Mon 25/11/24**	**Sat 25/12/20**	**###########**	**Sat 25/12/20**	**###########**	**Sat 25/12/20**	**0 days**		
291	Excavation and Lateral Support	NA	As Possible	8 days	Mon 25/11/24	Mon 25/12/1	Mon 25/11/24	Mon 25/12/1	Mon 25/11/24	Mon 25/12/1	0 days	0	289
292	Formwork Erection	NA	As Possible	12 days	Sun 25/11/30	Thu 25/12/11	Sun 25/11/30	Thu 25/12/11	Sun 25/11/30	Thu 25/12/11	0 days	0	291FS-2 days
293	Catchpit construcion	NA	As Possible	11 days	Wed 25/12/10	Sat 25/12/20	Wed 25/12/10	Sat 25/12/20	Wed 25/12/10	Sat 25/12/20	0 days	0	292FS-2 days
294	Concreting	NA	As Possible	1 day	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	Fri 25/12/19	0 days	0	293FS-2 days
295	**SHT.CP3.5~SHT.CP3.3,300->450CU(G),L=43.3**	**NA**	**As Possible**	**57 days**	**Sat 25/12/20**	**Sat 26/2/14**	**Sat 25/12/20**	**Sat 26/2/14**	**Sat 25/12/20**	**Sat 26/2/14**	**0 days**		
296	**Stage 1**	**NA**	**As Possible**	**29 days**	**Sat 25/12/20**	**Sat 26/1/17**	**Sat 25/12/20**	**Sat 26/1/17**	**Sat 25/12/20**	**Sat 26/1/17**	**0 days**		
297	Excavation and Lateral Support	NA	As Possible	10 days	Sat 25/12/20	Mon 25/12/29	Sat 25/12/20	Mon 25/12/29	Sat 25/12/20	Mon 25/12/29	0 days	0	294
298	Formwork Erection	NA	As Possible	12 days	Sun 25/12/28	Thu 26/1/8	Sun 25/12/28	Thu 26/1/8	Sun 25/12/28	Thu 26/1/8	0 days	0	297FS-2 days
299	Catchpit construcion	NA	As Possible	11 days	Wed 26/1/7	Sat 26/1/17	Wed 26/1/7	Sat 26/1/17	Wed 26/1/7	Sat 26/1/17	0 days	0	298FS-2 days
300	Concreting	NA	As Possible	1 day	Fri 26/1/16	Fri 26/1/16	Fri 26/1/16	Fri 26/1/16	Fri 26/1/16	Fri 26/1/16	0 days	0	299FS-2 days
301	**Stage 2**	**NA**	**As Possible**	**29 days**	**Sat 26/1/17**	**Sat 26/2/14**	**Sat 26/1/17**	**Sat 26/2/14**	**Sat 26/1/17**	**Sat 26/2/14**	**0 days**		
302	Excavation and Lateral Support	NA	As Possible	10 days	Sat 26/1/17	Mon 26/1/26	Sat 26/1/17	Mon 26/1/26	Sat 26/1/17	Mon 26/1/26	0 days	0	300
303	Formwork Erection	NA	As Possible	12 days	Sun 26/1/25	Thu 26/2/5	Sun 26/1/25	Thu 26/2/5	Sun 26/1/25	Thu 26/2/5	0 days	0	302FS-2 days
304	Catchpit construcion	NA	As Possible	11 days	Wed 26/2/4	Sat 26/2/14	Wed 26/2/4	Sat 26/2/14	Wed 26/2/4	Sat 26/2/14	0 days	0	303FS-2 days
305	Concreting	NA	As Possible	1 day	Fri 26/2/13	Fri 26/2/13	Fri 26/2/13	Fri 26/2/13	Fri 26/2/13	Fri 26/2/13	0 days	0	304FS-2 days
306	**End~SHT.CP3.5,300->450CU(G),L=107.7**	**NA**	**As Possible**	**113 days**	**Sat 26/2/14**	**Sat 26/6/6**	**Sat 26/2/14**	**Sat 26/6/6**	**Sat 26/2/14**	**Fri 27/4/2**	**0 days**		
307	**Stage 1**	**NA**	**As Possible**	**29 days**	**Sat 26/2/14**	**Sat 26/3/14**	**Sat 26/2/14**	**Sat 26/3/14**	**Sat 26/2/14**	**Sat 26/3/14**	**0 days**		
308	Excavation and Lateral Support	NA	As Possible	10 days	Sat 26/2/14	Mon 26/2/23	Sat 26/2/14	Mon 26/2/23	Sat 26/2/14	Mon 26/2/23	0 days	0	305
309	Formwork Erection	NA	As Possible	12 days	Sun 26/2/22	Thu 26/3/5	Sun 26/2/22	Thu 26/3/5	Sun 26/2/22	Thu 26/3/5	0 days	0	308FS-2 days
310	Catchpit construcion	NA	As Possible	11 days	Wed 26/3/4	Sat 26/3/14	Wed 26/3/4	Sat 26/3/14	Wed 26/3/4	Sat 26/3/14	0 days	0	309FS-2 days
311	Concreting	NA	As Possible	1 day	Fri 26/3/13	Fri 26/3/13	Fri 26/3/13	Fri 26/3/13	Fri 26/3/13	Fri 26/3/13	0 days	0	310FS-2 days
312	**Stage 2**	**NA**	**As Possible**	**29 days**	**Sat 26/3/14**	**Sat 26/4/11**	**Sat 26/3/14**	**Sat 26/4/11**	**Sat 26/3/14**	**Sat 26/4/11**	**0 days**		
313	Excavation and Lateral Support	NA	As Possible	10 days	Sat 26/3/14	Mon 26/3/23	Sat 26/3/14	Mon 26/3/23	Sat 26/3/14	Mon 26/3/23	0 days	0	311
314	Formwork Erection	NA	As Possible	12 days	Sun 26/3/22	Thu 26/4/2	Sun 26/3/22	Thu 26/4/2	Sun 26/3/22	Thu 26/4/2	0 days	0	313FS-2 days
315	Catchpit construcion	NA	As Possible	11 days	Wed 26/4/1	Sat 26/4/11	Wed 26/4/1	Sat 26/4/11	Wed 26/4/1	Sat 26/4/11	0 days	0	314FS-2 days
316	Concreting	NA	As Possible	1 day	Fri 26/4/10	Fri 26/4/10	Fri 26/4/10	Fri 26/4/10	Fri 26/4/10	Fri 26/4/10	0 days	0	315FS-2 days
317	**Stage 3**	**NA**	**As Possible**	**29 days**	**Sat 26/4/11**	**Sat 26/5/9**	**Sat 26/4/11**	**Sat 26/5/9**	**Sat 26/4/11**	**Sat 26/5/9**	**0 days**		
318	Excavation and Lateral Support	NA	As Possible	10 days	Sat 26/4/11	Mon 26/4/20	Sat 26/4/11	Mon 26/4/20	Sat 26/4/11	Mon 26/4/20	0 days	0	316
319	Formwork Erection	NA	As Possible	12 days	Sun 26/4/19	Thu 26/4/30	Sun 26/4/19	Thu 26/4/30	Sun 26/4/19	Thu 26/4/30	0 days	0	318FS-2 days
320	Catchpit construcion	NA	As Possible	11 days	Wed 26/4/29	Sat 26/5/9	Wed 26/4/29	Sat 26/5/9	Wed 26/4/29	Sat 26/5/9	0 days	0	319FS-2 days
321	Concreting	NA	As Possible	1 day	Fri 26/5/8	Fri 26/5/8	Fri 26/5/8	Fri 26/5/8	Fri 26/5/8	Fri 26/5/8	0 days	0	320FS-2 days
322	**Stage 4**	**NA**	**As Possible**	**29 days**	**Sat 26/5/9**	**Sat 26/6/6**	**Sat 26/5/9**	**Sat 26/6/6**	**Sat 26/5/9**	**Fri 27/4/2**	**0 days**		
323	Excavation and Lateral Support	NA	As Possible	10 days	Sat 26/5/9	Mon 26/5/18	Sat 26/5/9	Mon 26/5/18	Sat 26/5/9	Mon 26/5/18	0 days	0	321
324	Formwork Erection	NA	As Possible	12 days	Sun 26/5/17	Thu 26/5/28	Sun 26/5/17	Thu 26/5/28	Sun 26/5/17	Thu 26/5/28	0 days	0	323FS-2 days
325	Catchpit construcion	NA	As Possible	11 days	Wed 26/5/27	Sat 26/6/6	Wed 26/5/27	Sat 26/6/6	Wed 26/5/27	Sat 26/6/6	0 days	0	324FS-2 days
326	Concreting	NA	As Possible	1 day	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	Fri 27/4/2	Fri 27/4/2	301 days	0	325FS-2 days
327	**U-Channel Works (East)**	**NA**	**As Possible**	**570 days**	**Wed 24/11/13**	**Fri 26/6/5**	**Wed 24/11/13**	**Fri 26/6/5**	**Wed 24/11/13**	**Fri 26/6/5**	**0 days**		
328	**SHT.CP11~SHT.CP10E,750CU(HD-G),L=19.8**	**NA**	**As Possible**	**30 days**	**Wed 24/11/13**	**Thu 24/12/12**	**Wed 24/11/13**	**Thu 24/12/12**	**Wed 24/11/13**	**Thu 24/12/12**	**0 days**		
329	Excavation and Lateral Support	NA	As Possible	11 days	Wed 24/11/13	Sat 24/11/23	Wed 24/11/13	Sat 24/11/23	Wed 24/11/13	Sat 24/11/23	0 days	0	239SS-126 day
330	Formwork Erection	NA	As Possible	12 days	Fri 24/11/22	Tue 24/12/3	Fri 24/11/22	Tue 24/12/3	Fri 24/11/22	Tue 24/12/3	0 days	0	329FS-2 days
331	Catchpit construcion	NA	As Possible	11 days	Mon 24/12/2	Thu 24/12/12	Mon 24/12/2	Thu 24/12/12	Mon 24/12/2	Thu 24/12/12	0 days	0	330FS-2 days
332	Concreting	NA	As Possible	1 day	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	0 days	0	331FS-2 days
333	**SHT.CP10E~SHT.CP10D,750CU(HD-G),L=23.7**	**NA**	**As Possible**	**36 days**	**Thu 24/12/12**	**Thu 25/1/16**	**Thu 24/12/12**	**Thu 25/1/16**	**Thu 24/12/12**	**Thu 25/1/16**	**0 days**		
334	Excavation and Lateral Support	NA	As Possible	13 days	Thu 24/12/12	Tue 24/12/24	Thu 24/12/12	Tue 24/12/24	Thu 24/12/12	Tue 24/12/24	0 days	0	332
335	Formwork Erection	NA	As Possible	14 days	Mon 24/12/23	Sun 25/1/5	Mon 24/12/23	Sun 25/1/5	Mon 24/12/23	Sun 25/1/5	0 days	0	334FS-2 days
336	Catchpit construcion	NA	As Possible	13 days	Sat 25/1/4	Thu 25/1/16	Sat 25/1/4	Thu 25/1/16	Sat 25/1/4	Thu 25/1/16	0 days	0	335FS-2 days
337	Concreting	NA	As Possible	1 day	Wed 25/1/15	Wed 25/1/15	Wed 25/1/15	Wed 25/1/15	Wed 25/1/15	Wed 25/1/15	0 days	0	336FS-2 days
338	**SHT.CP10D~SHT.CP10C,750CU(HD-G),L=11.9**	**NA**	**As Possible**	**24 days**	**Thu 25/1/16**	**Sat 25/2/8**	**Thu 25/1/16**	**Sat 25/2/8**	**Thu 25/1/16**	**Sat 25/2/8**	**0 days**		
339	Excavation and Lateral Support	NA	As Possible	8 days	Thu 25/1/16	Thu 25/1/23	Thu 25/1/16	Thu 25/1/23	Thu 25/1/16	Thu 25/1/23	0 days	0	337
340	Formwork Erection	NA	As Possible	10 days	Wed 25/1/22	Fri 25/1/31	Wed 25/1/22	Fri 25/1/31	Wed 25/1/22	Fri 25/1/31	0 days	0	339FS-2 days
341	Catchpit construcion	NA	As Possible	10 days	Thu 25/1/30	Sat 25/2/8	Thu 25/1/30	Sat 25/2/8	Thu 25/1/30	Sat 25/2/8	0 days	0	340FS-2 days
342	Concreting	NA	As Possible	1 day	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	Fri 25/2/7	0 days	0	341FS-2 days
343	**SHT.CP10C~SHT.CP10B,750CU(HD-G),L=6.5**	**NA**	**As Possible**	**17 days**	**Sat 25/2/8**	**Mon 25/2/24**	**Sat 25/2/8**	**Mon 25/2/24**	**Sat 25/2/8**	**Mon 25/2/24**	**0 days**		
344	Excavation and Lateral Support	NA	As Possible	6 days	Sat 25/2/8	Thu 25/2/13	Sat 25/2/8	Thu 25/2/13	Sat 25/2/8	Thu 25/2/13	0 days	0	342
345	Formwork Erection	NA	As Possible	8 days	Wed 25/2/12	Wed 25/2/19	Wed 25/2/12	Wed 25/2/19	Wed 25/2/12	Wed 25/2/19	0 days	0	344FS-2 days
346	Catchpit construcion	NA	As Possible	7 days	Tue 25/2/18	Mon 25/2/24	Tue 25/2/18	Mon 25/2/24	Tue 25/2/18	Mon 25/2/24	0 days	0	345FS-2 days
347	Concreting	NA	As Possible	1 day	Sun 25/2/23	Sun 25/2/23	Sun 25/2/23	Sun 25/2/23	Sun 25/2/23	Sun 25/2/23	0 days	0	346FS-2 days
348	**SHT.CP10B~SHT.CP10A,750CU(HD-G),L=6.4**	**NA**	**As Possible**	**17 days**	**Mon 25/2/24**	**Wed 25/3/12**	**Mon 25/2/24**	**Wed 25/3/12**	**Mon 25/2/24**	**Wed 25/3/12**	**0 days**		
349	Excavation and Lateral Support	NA	As Possible	6 days	Mon 25/2/24	Sat 25/3/1	Mon 25/2/24	Sat 25/3/1	Mon 25/2/24	Sat 25/3/1	0 days	0	347
350	Formwork Erection	NA	As Possible	8 days	Fri 25/2/28	Fri 25/3/7	Fri 25/2/28	Fri 25/3/7	Fri 25/2/28	Fri 25/3/7	0 days	0	349FS-2 days
351	Catchpit construcion	NA	As Possible	7 days	Thu 25/3/6	Wed 25/3/12	Thu 25/3/6	Wed 25/3/12	Thu 25/3/6	Wed 25/3/12	0 days	0	350FS-2 days
352	Concreting	NA	As Possible	1 day	Tue 25/3/11	Tue 25/3/11	Tue 25/3/11	Tue 25/3/11	Tue 25/3/11	Tue 25/3/11	0 days	0	351FS-2 days
353	**SHT.CP10A~SHT.CP10,750CU(HD-G),L=26.7**	**NA**	**As Possible**	**39 days**	**Wed 25/3/12**	**Sat 25/4/19**	**Wed 25/3/12**	**Sat 25/4/19**	**Wed 25/3/12**	**Sat 25/4/19**	**0 days**		
354	Excavation and Lateral Support	NA	As Possible	14 days	Wed 25/3/12	Tue 25/3/25	Wed 25/3/12	Tue 25/3/25	Wed 25/3/12	Tue 25/3/25	0 days	0	352
355	Formwork Erection	NA	As Possible	15 days	Mon 25/3/24	Mon 25/4/7	Mon 25/3/24	Mon 25/4/7	Mon 25/3/24	Mon 25/4/7	0 days	0	354FS-2 days
356	Catchpit construcion	NA	As Possible	14 days	Sun 25/4/6	Sat 25/4/19	Sun 25/4/6	Sat 25/4/19	Sun 25/4/6	Sat 25/4/19	0 days	0	355FS-2 days
357	Concreting	NA	As Possible	1 day	Fri 25/4/18	Fri 25/4/18	Fri 25/4/18	Fri 25/4/18	Fri 25/4/18	Fri 25/4/18	0 days	0	356FS-2 days
358	**SHT.CP10~SHT.CP9,750CU(HD-G),L=4.3**	**NA**	**As Possible**	**17 days**	**Sat 25/4/19**	**Mon 25/5/5**	**Sat 25/4/19**	**Mon 25/5/5**	**Sat 25/4/19**	**Mon 25/5/5**	**0 days**		
359	Excavation and Lateral Support	NA	As Possible	6 days	Sat 25/4/19	Thu 25/4/24	Sat 25/4/19	Thu 25/4/24	Sat 25/4/19	Thu 25/4/24	0 days	0	357
360	Formwork Erection	NA	As Possible	8 days	Wed 25/4/23	Wed 25/4/30	Wed 25/4/23	Wed 25/4/30	Wed 25/4/23	Wed 25/4/30	0 days	0	359FS-2 days
361	Catchpit construcion	NA	As Possible	7 days	Tue 25/4/29	Mon 25/5/5	Tue 25/4/29	Mon 25/5/5	Tue 25/4/29	Mon 25/5/5	0 days	0	360FS-2 days
362	Concreting	NA	As Possible	1 day	Sun 25/5/4	Sun 25/5/4	Sun 25/5/4	Sun 25/5/4	Sun 25/5/4	Sun 25/5/4	0 days	0	361FS-2 days
363	**SHT.CP9~SHT.CP8,600CU(HD-G),L=33.7**	**NA**	**As Possible**	**45 days**	**Mon 25/5/5**	**Wed 25/6/18**	**Mon 25/5/5**	**Wed 25/6/18**	**Mon 25/5/5**	**Wed 25/6/18**	**0 days**		
364	**Stage 1**	**NA**	**As Possible**	**24 days**	**Mon 25/5/5**	**Wed 25/5/28**	**Mon 25/5/5**	**Wed 25/5/28**	**Mon 25/5/5**	**Wed 25/5/28**	**0 days**		

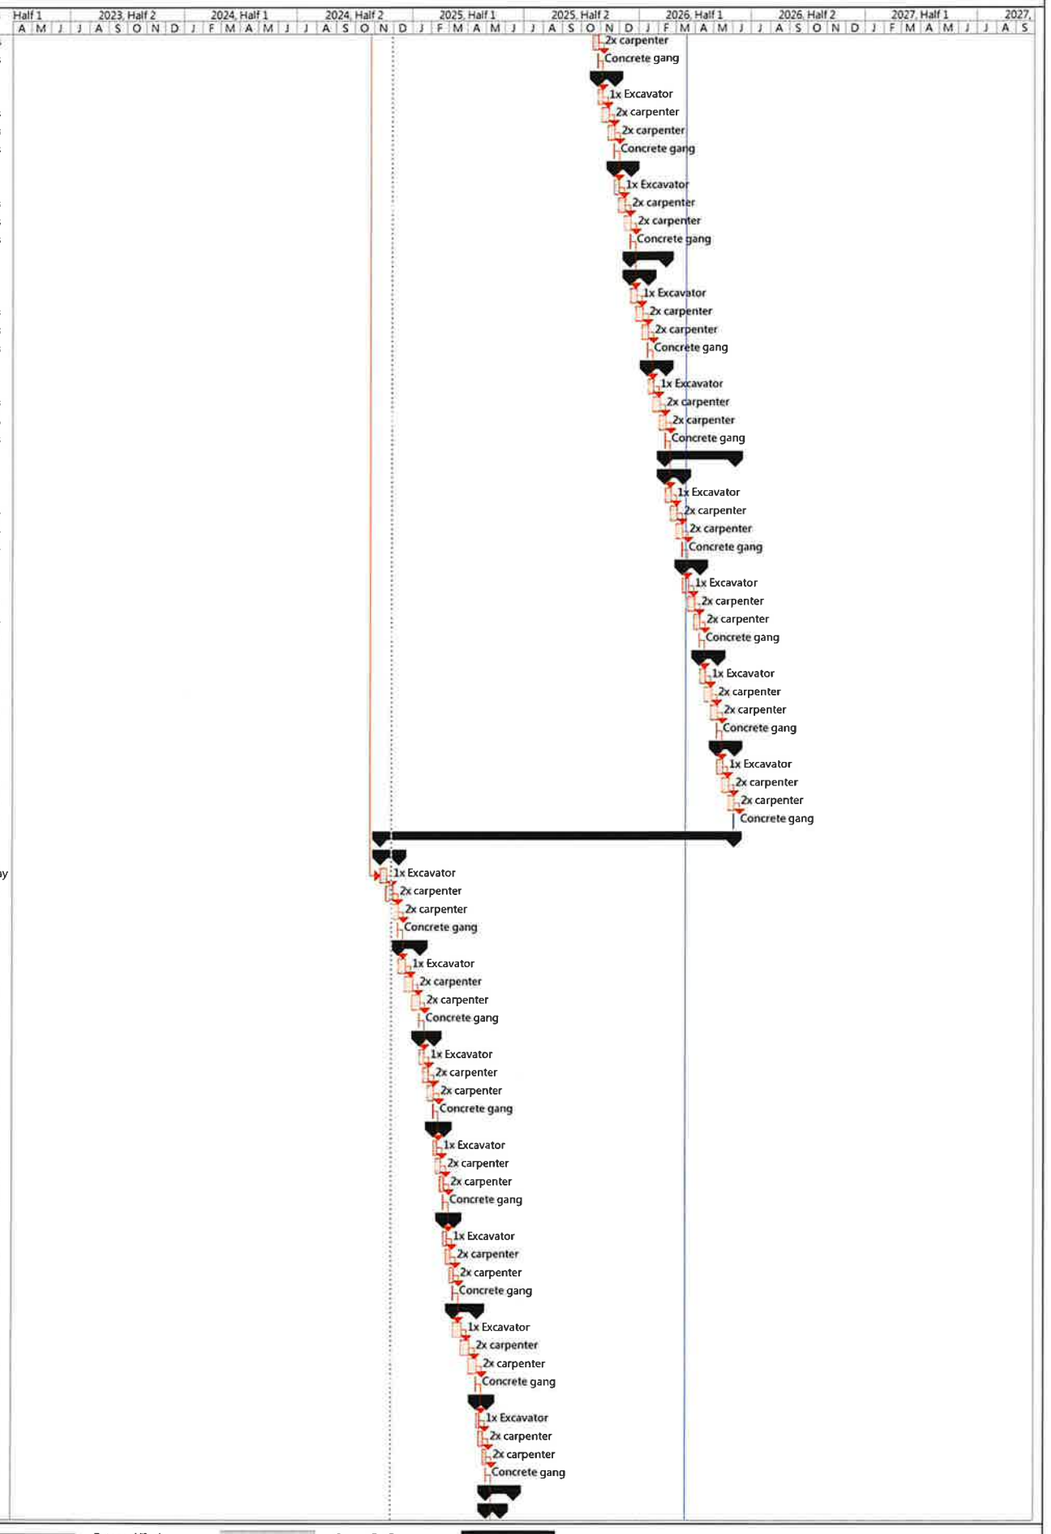


Revision.: 14.0 Date: 31 October 2024

Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)
U-Channel: {U/S}~{D/S},size+type,length(m)
Drainage Channel: {U/S}~{D/S}

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
365	Excavation and Lateral Support	NA	As Possible	8 days	Mon 25/5/5	Mon 25/5/12	Mon 25/5/5	Mon 25/5/12	Mon 25/5/5	Mon 25/5/12	0 days	0	362
366	Formwork Erection	NA	As Possible	10 days	Sun 25/5/11	Tue 25/5/20	Sun 25/5/11	Tue 25/5/20	Sun 25/5/11	Tue 25/5/20	0 days	0	365FS-2 days
367	Catchpit construcion	NA	As Possible	10 days	Mon 25/5/19	Wed 25/5/28	Mon 25/5/19	Wed 25/5/28	Mon 25/5/19	Wed 25/5/28	0 days	0	366FS-2 days
368	Concreting	NA	As Possible	1 day	Tue 25/5/27	Tue 25/5/27	Tue 25/5/27	Tue 25/5/27	Tue 25/5/27	Tue 25/5/27	0 days	0	367FS-2 days
369	**Stage 2**	**NA**	**As Possible**	**22 days**	**Wed 25/5/28**	**Wed 25/6/18**	**Wed 25/5/28**	**Wed 25/6/18**	**Wed 25/5/28**	**Wed 25/6/18**	**0 days**		
370	Excavation and Lateral Support	NA	As Possible	8 days	Wed 25/5/28	Wed 25/6/4	Wed 25/5/28	Wed 25/6/4	Wed 25/5/28	Wed 25/6/4	0 days	0	368
371	Formwork Erection	NA	As Possible	10 days	Tue 25/6/3	Thu 25/6/12	Tue 25/6/3	Thu 25/6/12	Tue 25/6/3	Thu 25/6/12	0 days	0	370FS-2 days
372	Catchpit construcion	NA	As Possible	8 days	Wed 25/6/11	Wed 25/6/18	Wed 25/6/11	Wed 25/6/18	Wed 25/6/11	Wed 25/6/18	0 days	0	371FS-2 days
373	Concreting	NA	As Possible	1 day	Tue 25/6/17	Tue 25/6/17	Tue 25/6/17	Tue 25/6/17	Tue 25/6/17	Tue 25/6/17	0 days	0	372FS-2 days
374	Connection of ex. 300CU to SHT.CP8	Fri 26/6/5	Later Than	28 days	Mon 25/6/16	Sun 25/7/13	Mon 25/6/16	Sun 25/7/13	Sat 26/5/9	Fri 26/6/5	327 days	0	373FS-2 days
375	**SHT.CP8~SHT.CP7,600CU(HD-G),L=8.5**	**NA**	**As Possible**	**17 days**	**Wed 25/6/18**	**Fri 25/7/4**	**Wed 25/6/18**	**Fri 25/7/4**	**Wed 25/6/18**	**Fri 25/7/4**	**0 days**		
376	Excavation and Lateral Support	NA	As Possible	6 days	Wed 25/6/18	Mon 25/6/23	Wed 25/6/18	Mon 25/6/23	Wed 25/6/18	Mon 25/6/23	0 days	0	373
377	Formwork Erection	NA	As Possible	8 days	Sun 25/6/22	Sun 25/6/29	Sun 25/6/22	Sun 25/6/29	Sun 25/6/22	Sun 25/6/29	0 days	0	376FS-2 days
378	Catchpit construcion	NA	As Possible	7 days	Sat 25/6/28	Fri 25/7/4	Sat 25/6/28	Fri 25/7/4	Sat 25/6/28	Fri 25/7/4	0 days	0	377FS-2 days
379	Concreting	NA	As Possible	1 day	Thu 25/7/3	Thu 25/7/3	Thu 25/7/3	Thu 25/7/3	Thu 25/7/3	Thu 25/7/3	0 days	0	378FS-2 days
380	Reconstruction of U/S end wall	Fri 26/6/5	Later Than	21 days	Wed 25/7/2	Tue 25/7/22	Wed 25/7/2	Tue 25/7/22	Sat 26/5/16	Fri 26/6/5	318 days	0	379FS-2 days
381	**SHT.CP7~SHT.CP6,600CU(HD-G),L=130.8**	**NA**	**As Possible**	**141 days**	**Fri 25/7/4**	**Fri 25/11/21**	**Fri 25/7/4**	**Fri 25/11/21**	**Fri 25/7/4**	**Fri 25/11/21**	**0 days**		
382	**Stage 1**	**NA**	**As Possible**	**29 days**	**Fri 25/7/4**	**Fri 25/8/1**	**Fri 25/7/4**	**Fri 25/8/1**	**Fri 25/7/4**	**Fri 25/8/1**	**0 days**		
383	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/7/4	Sun 25/7/13	Fri 25/7/4	Sun 25/7/13	Fri 25/7/4	Sun 25/7/13	0 days	0	379
384	Formwork Erection	NA	As Possible	12 days	Sat 25/7/12	Wed 25/7/23	Sat 25/7/12	Wed 25/7/23	Sat 25/7/12	Wed 25/7/23	0 days	0	383FS-2 days
385	Catchpit construcion	NA	As Possible	11 days	Tue 25/7/22	Fri 25/8/1	Tue 25/7/22	Fri 25/8/1	Tue 25/7/22	Fri 25/8/1	0 days	0	384FS-2 days
386	Concreting	NA	As Possible	1 day	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	0 days	0	385FS-2 days
387	**Stage 2**	**NA**	**As Possible**	**29 days**	**Fri 25/8/1**	**Fri 25/8/29**	**Fri 25/8/1**	**Fri 25/8/29**	**Fri 25/8/1**	**Fri 25/8/29**	**0 days**		
388	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/8/1	Sun 25/8/10	Fri 25/8/1	Sun 25/8/10	Fri 25/8/1	Sun 25/8/10	0 days	0	386
389	Formwork Erection	NA	As Possible	12 days	Sat 25/8/9	Wed 25/8/20	Sat 25/8/9	Wed 25/8/20	Sat 25/8/9	Wed 25/8/20	0 days	0	388FS-2 days
390	Catchpit construcion	NA	As Possible	11 days	Tue 25/8/19	Fri 25/8/29	Tue 25/8/19	Fri 25/8/29	Tue 25/8/19	Fri 25/8/29	0 days	0	389FS-2 days
391	Concreting	NA	As Possible	1 day	Thu 25/8/28	Thu 25/8/28	Thu 25/8/28	Thu 25/8/28	Thu 25/8/28	Thu 25/8/28	0 days	0	390FS-2 days
392	**Stage 3**	**NA**	**As Possible**	**29 days**	**Fri 25/8/29**	**Fri 25/9/26**	**Fri 25/8/29**	**Fri 25/9/26**	**Fri 25/8/29**	**Fri 25/9/26**	**0 days**		
393	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/8/29	Sun 25/9/7	Fri 25/8/29	Sun 25/9/7	Fri 25/8/29	Sun 25/9/7	0 days	0	391
394	Formwork Erection	NA	As Possible	12 days	Sat 25/9/6	Wed 25/9/17	Sat 25/9/6	Wed 25/9/17	Sat 25/9/6	Wed 25/9/17	0 days	0	393FS-2 days
395	Catchpit construcion	NA	As Possible	11 days	Tue 25/9/16	Fri 25/9/26	Tue 25/9/16	Fri 25/9/26	Tue 25/9/16	Fri 25/9/26	0 days	0	394FS-2 days
396	Concreting	NA	As Possible	1 day	Thu 25/9/25	Thu 25/9/25	Thu 25/9/25	Thu 25/9/25	Thu 25/9/25	Thu 25/9/25	0 days	0	395FS-2 days
397	**Stage 4**	**NA**	**As Possible**	**29 days**	**Fri 25/9/26**	**Fri 25/10/24**	**Fri 25/9/26**	**Fri 25/10/24**	**Fri 25/9/26**	**Fri 25/10/24**	**0 days**		
398	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/9/26	Sun 25/10/5	Fri 25/9/26	Sun 25/10/5	Fri 25/9/26	Sun 25/10/5	0 days	0	396
399	Formwork Erection	NA	As Possible	12 days	Sat 25/10/4	Wed 25/10/15	Sat 25/10/4	Wed 25/10/15	Sat 25/10/4	Wed 25/10/15	0 days	0	398FS-2 days
400	Catchpit construcion	NA	As Possible	11 days	Tue 25/10/14	Fri 25/10/24	Tue 25/10/14	Fri 25/10/24	Tue 25/10/14	Fri 25/10/24	0 days	0	399FS-2 days
401	Concreting	NA	As Possible	1 day	Thu 25/10/23	Thu 25/10/23	Thu 25/10/23	Thu 25/10/23	Thu 25/10/23	Thu 25/10/23	0 days	0	400FS-2 days
402	**Stage 5**	**NA**	**As Possible**	**29 days**	**Fri 25/10/24**	**Fri 25/11/21**	**Fri 25/10/24**	**Fri 25/11/21**	**Fri 25/10/24**	**Fri 25/11/21**	**0 days**		
403	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/10/24	Sun 25/11/2	Fri 25/10/24	Sun 25/11/2	Fri 25/10/24	Sun 25/11/2	0 days	0	401
404	Formwork Erection	NA	As Possible	12 days	Sat 25/11/1	Wed 25/11/12	Sat 25/11/1	Wed 25/11/12	Sat 25/11/1	Wed 25/11/12	0 days	0	403FS-2 days
405	Catchpit construcion	NA	As Possible	11 days	Tue 25/11/11	Fri 25/11/21	Tue 25/11/11	Fri 25/11/21	Tue 25/11/11	Fri 25/11/21	0 days	0	404FS-2 days
406	Concreting	NA	As Possible	1 day	Thu 25/11/20	Thu 25/11/20	Thu 25/11/20	Thu 25/11/20	Thu 25/11/20	Thu 25/11/20	0 days	0	405FS-2 days
407	Connection of ex. 400CU to SHT.CP6	Fri 26/6/5	Later Than	28 days	Wed 25/11/19	Tue 25/12/16	Wed 25/11/19	Tue 25/12/16	Sat 26/5/9	Fri 26/6/5	171 days	0	406FS-2 days
408	**SHT.CP6~SHT.CP5,600CU(HD-G),L=24.1**	**NA**	**As Possible**	**36 days**	**Fri 25/11/21**	**Fri 25/12/26**	**Fri 25/11/21**	**Fri 25/12/26**	**Fri 25/11/21**	**Fri 25/12/26**	**0 days**		
409	Excavation and Lateral Support	NA	As Possible	13 days	Fri 25/11/21	Wed 25/12/3	Fri 25/11/21	Wed 25/12/3	Fri 25/11/21	Wed 25/12/3	0 days	0	406
410	Formwork Erection	NA	As Possible	14 days	Tue 25/12/2	Mon 25/12/15	Tue 25/12/2	Mon 25/12/15	Tue 25/12/2	Mon 25/12/15	0 days	0	409FS-2 days
411	Catchpit construcion	NA	As Possible	13 days	Sun 25/12/14	Fri 25/12/26	Sun 25/12/14	Fri 25/12/26	Sun 25/12/14	Fri 25/12/26	0 days	0	410FS-2 days
412	Concreting	NA	As Possible	1 day	Thu 25/12/25	Thu 25/12/25	Thu 25/12/25	Thu 25/12/25	Thu 25/12/25	Thu 25/12/25	0 days	0	411FS-2 days
413	Connection of ex. 400CU to SHT.CP5	Fri 26/6/5	Later Than	28 days	Wed 25/12/24	Tue 26/1/20	Wed 25/12/24	Tue 26/1/20	Sat 26/5/9	Fri 26/6/5	136 days	0	412FS-2 days
414	**SHT.CP5~SHT.CP4,600CU(HD-G),L=73.9**	**NA**	**As Possible**	**85 days**	**Fri 25/12/26**	**Fri 26/3/20**	**Fri 25/12/26**	**Fri 26/3/20**	**Fri 25/12/26**	**Fri 26/3/20**	**0 days**		
415	**Stage 1**	**NA**	**As Possible**	**29 days**	**Fri 25/12/26**	**Fri 26/1/23**	**Fri 25/12/26**	**Fri 26/1/23**	**Fri 25/12/26**	**Fri 26/1/23**	**0 days**		
416	Excavation and Lateral Support	NA	As Possible	10 days	Fri 25/12/26	Sun 26/1/4	Fri 25/12/26	Sun 26/1/4	Fri 25/12/26	Sun 26/1/4	0 days	0	412
417	Formwork Erection	NA	As Possible	12 days	Sat 26/1/3	Wed 26/1/14	Sat 26/1/3	Wed 26/1/14	Sat 26/1/3	Wed 26/1/14	0 days	0	416FS-2 days
418	Catchpit construcion	NA	As Possible	11 days	Tue 26/1/13	Fri 26/1/23	Tue 26/1/13	Fri 26/1/23	Tue 26/1/13	Fri 26/1/23	0 days	0	417FS-2 days
419	Concreting	NA	As Possible	1 day	Thu 26/1/22	Thu 26/1/22	Thu 26/1/22	Thu 26/1/22	Thu 26/1/22	Thu 26/1/22	0 days	0	418FS-2 days
420	**Stage 2**	**NA**	**As Possible**	**29 days**	**Fri 26/1/23**	**Fri 26/2/20**	**Fri 26/1/23**	**Fri 26/2/20**	**Fri 26/1/23**	**Fri 26/2/20**	**0 days**		
421	Excavation and Lateral Support	NA	As Possible	10 days	Fri 26/1/23	Sun 26/2/1	Fri 26/1/23	Sun 26/2/1	Fri 26/1/23	Sun 26/2/1	0 days	0	419
422	Formwork Erection	NA	As Possible	12 days	Sat 26/1/31	Wed 26/2/11	Sat 26/1/31	Wed 26/2/11	Sat 26/1/31	Wed 26/2/11	0 days	0	421FS-2 days
423	Catchpit construcion	NA	As Possible	11 days	Tue 26/2/10	Fri 26/2/20	Tue 26/2/10	Fri 26/2/20	Tue 26/2/10	Fri 26/2/20	0 days	0	422FS-2 days
424	Concreting	NA	As Possible	1 day	Thu 26/2/19	Thu 26/2/19	Thu 26/2/19	Thu 26/2/19	Thu 26/2/19	Thu 26/2/19	0 days	0	423FS-2 days
425	**Stage 3**	**NA**	**As Possible**	**29 days**	**Fri 26/2/20**	**Fri 26/3/20**	**Fri 26/2/20**	**Fri 26/3/20**	**Fri 26/2/20**	**Fri 26/3/20**	**0 days**		
426	Excavation and Lateral Support	NA	As Possible	10 days	Fri 26/2/20	Sun 26/3/1	Fri 26/2/20	Sun 26/3/1	Fri 26/2/20	Sun 26/3/1	0 days	0	424
427	Formwork Erection	NA	As Possible	12 days	Sat 26/2/28	Wed 26/3/11	Sat 26/2/28	Wed 26/3/11	Sat 26/2/28	Wed 26/3/11	0 days	0	426FS-2 days
428	Catchpit construcion	NA	As Possible	11 days	Tue 26/3/10	Fri 26/3/20	Tue 26/3/10	Fri 26/3/20	Tue 26/3/10	Fri 26/3/20	0 days	0	427FS-2 days
429	Concreting	NA	As Possible	1 day	Thu 26/3/19	Thu 26/3/19	Thu 26/3/19	Thu 26/3/19	Thu 26/3/19	Thu 26/3/19	0 days	0	428FS-2 days
430	Connection of ex. 450CU to SHT.CP4	Fri 26/6/5	Later Than	28 days	Wed 26/3/18	Tue 26/4/14	Wed 26/3/18	Tue 26/4/14	Sat 26/5/9	Fri 26/6/5	52 days	0	429FS-2 days
431	**SHT.CP4~End,525CU(HD-G),L=82.3**	**NA**	**As Possible**	**78 days**	**Fri 26/3/20**	**Fri 26/6/5**	**Fri 26/3/20**	**Fri 26/6/5**	**Fri 26/3/20**	**Fri 26/6/5**	**0 days**		
432	**Stage 1**	**NA**	**As Possible**	**27 days**	**Fri 26/3/20**	**Wed 26/4/15**	**Fri 26/3/20**	**Wed 26/4/15**	**Fri 26/3/20**	**Wed 26/4/15**	**0 days**		
433	Excavation and Lateral Support	NA	As Possible	10 days	Fri 26/3/20	Sun 26/3/29	Fri 26/3/20	Sun 26/3/29	Fri 26/3/20	Sun 26/3/29	0 days	0	429,115,118
434	Formwork Erection	NA	As Possible	11 days	Sat 26/3/28	Tue 26/4/7	Sat 26/3/28	Tue 26/4/7	Sat 26/3/28	Tue 26/4/7	0 days	0	433FS-2 days
435	Catchpit construcion	NA	As Possible	10 days	Mon 26/4/6	Wed 26/4/15	Mon 26/4/6	Wed 26/4/15	Mon 26/4/6	Wed 26/4/15	0 days	0	434FS-2 days
436	Concreting	NA	As Possible	1 day	Tue 26/4/14	Tue 26/4/14	Tue 26/4/14	Tue 26/4/14	Tue 26/4/14	Tue 26/4/14	0 days	0	435FS-2 days
437	**Stage 2**	**NA**	**As Possible**	**27 days**	**Wed 26/4/15**	**Mon 26/5/11**	**Wed 26/4/15**	**Mon 26/5/11**	**Wed 26/4/15**	**Mon 26/5/11**	**0 days**		
438	Excavation and Lateral Support	NA	As Possible	10 days	Wed 26/4/15	Fri 26/4/24	Wed 26/4/15	Fri 26/4/24	Wed 26/4/15	Fri 26/4/24	0 days	0	436
439	Formwork Erection	NA	As Possible	11 days	Thu 26/4/23	Sun 26/5/3	Thu 26/4/23	Sun 26/5/3	Thu 26/4/23	Sun 26/5/3	0 days	0	438FS-2 days
440	Catchpit construcion	NA	As Possible	10 days	Sat 26/5/2	Mon 26/5/11	Sat 26/5/2	Mon 26/5/11	Sat 26/5/2	Mon 26/5/11	0 days	0	439FS-2 days
441	Concreting	NA	As Possible	1 day	Sun 26/5/10	Sun 26/5/10	Sun 26/5/10	Sun 26/5/10	Sun 26/5/10	Sun 26/5/10	0 days	0	440FS-2 days
442	**Stage 3**	**NA**	**As Possible**	**26 days**	**Mon 26/5/11**	**Fri 26/6/5**	**Mon 26/5/11**	**Fri 26/6/5**	**Mon 26/5/11**	**Fri 26/6/5**	**0 days**		
443	Excavation and Lateral Support	NA	As Possible	10 days	Mon 26/5/11	Wed 26/5/20	Mon 26/5/11	Wed 26/5/20	Mon 26/5/11	Wed 26/5/20	0 days	0	441
444	Formwork Erection	NA	As Possible	10 days	Tue 26/5/19	Thu 26/5/28	Tue 26/5/19	Thu 26/5/28	Tue 26/5/19	Thu 26/5/28	0 days	0	443FS-2 days
445	Catchpit construcion	NA	As Possible	10 days	Wed 26/5/27	Fri 26/6/5	Wed 26/5/27	Fri 26/6/5	Wed 26/5/27	Fri 26/6/5	0 days	0	444FS-2 days
446	Concreting	Fri 26/6/5	Later Than	1 day	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	Fri 26/6/5	0 days	0	445FS-1 day

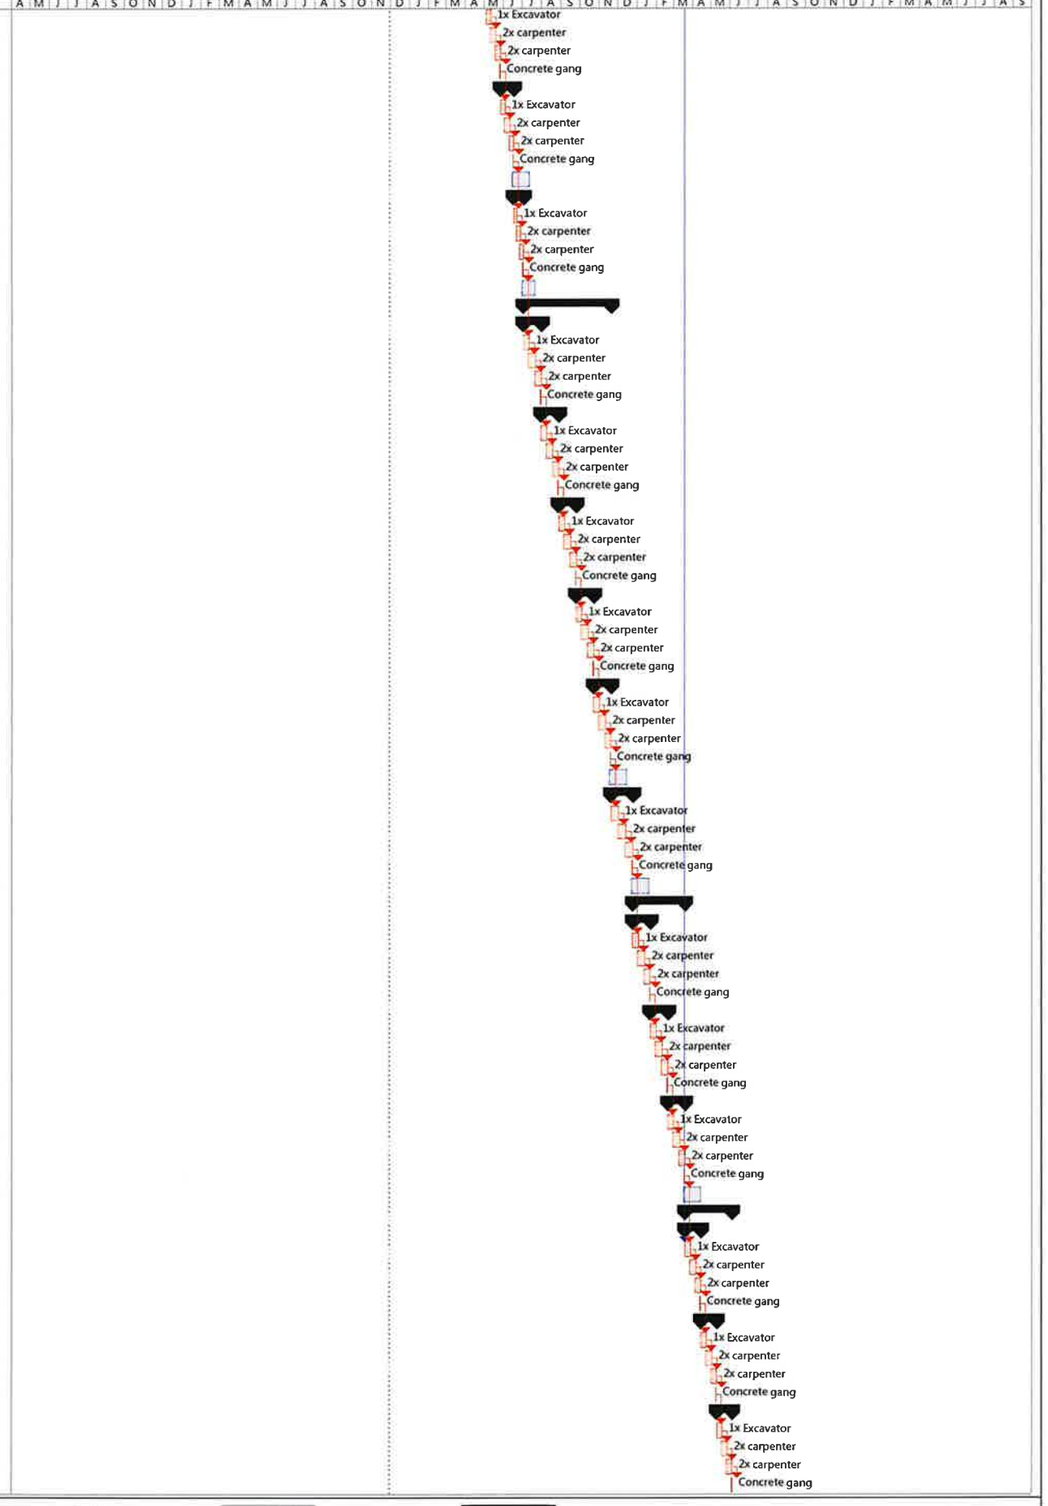

Appendix 1.2 Project Organization Chart


Appendix 1

Wing Tat Civil Engineering Co. Ltd

Contract No. : DC/2022/02

Drainage Improvement Works at Yuen Long – Stage 2

Organization Chart of Environmental Management (updated on 12-06-2024)

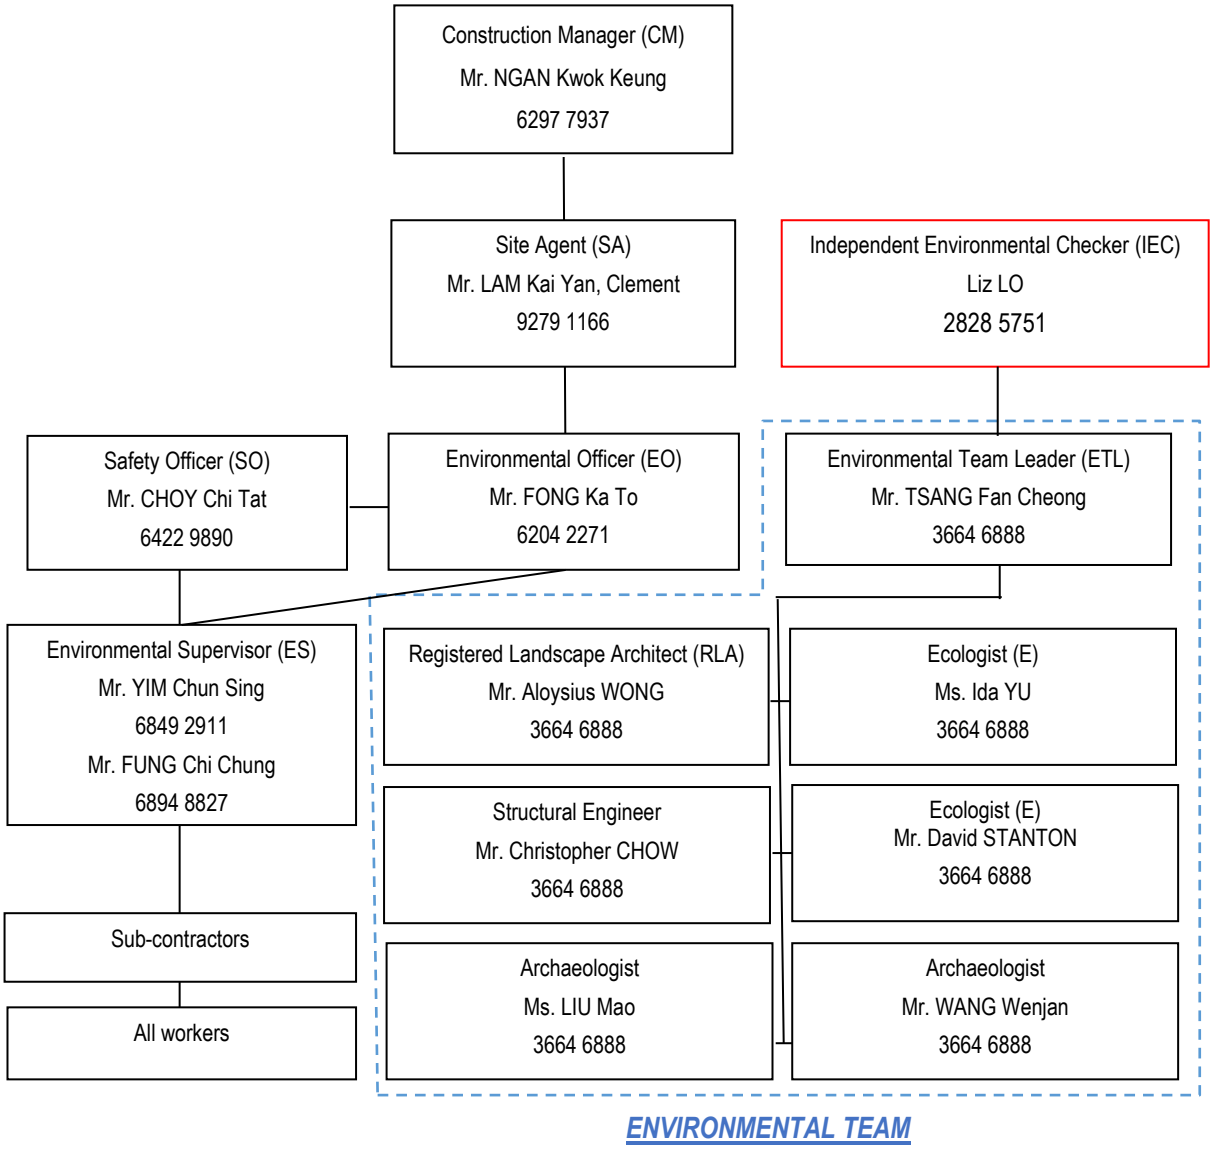

Appendix 1.3 Implementation Status of Environmental Mitigation Measures

Air Quality Impact Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
S.3.8.1	S.3.2.3	All the dust control measures as recommended in the Air Pollution Control (Construction Dust) Regulation, where applicable, should be implemented. Typical dust control measures include:	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• Proper and regular watering should be provided for all exposed and excavated work sites.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• Open stockpiles should be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• All excavated or stockpile of dusty materials should be entirely covered by impervious sheeting or sprayed with water to ensure that the entire surface is wet. They should be sprayed with water immediately prior to any loading or transfer activities. These materials should be removed, backfilled or reinstated where practicable.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.3.8.1	S.3.2.3	• After the removal of stockpiles, the remaining dusty material should be sprayed with water and cleared from the surface of roads. Stockpiling areas of dusty materials should not be extended beyond the pedestrian barriers, fencing or traffic cones.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• At locations with proposed open excavation and reinstatement works, hoarding of not less than 2.4 m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit. The contractor should ensure that the hoardings are well maintained throughout the entire construction period.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• Vehicles used for the transportation of dusty materials/ spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• Vehicle wheel washing facilities will be provided at exit of the works site. The areas where vehicle wheel washing activities are carried out and the section of the construction site between the vehicle washing facilities and the exit should be paved with concrete or bituminous materials.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.3.8.1	S.3.2.3	• Where possible, routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• All demolished materials that may generate dust should be covered entirely by impervious sheeting or placed in a covered area with the top and three sides enclosed within a day of demolition.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• At construction works areas where demolition takes place, water or dust suppression chemicals should be sprayed prior to, during and immediately after the demolition activities to ensure that the top surface remains wet.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• The requirements stipulated in the Development Bureau Technical Circular (Works) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness should be followed as far as practicable to enhance the cleanliness and tidiness of construction sites.	Air Quality (fugitive dust) Control during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Development Bureau Technical Circular (Works) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.3.8.1	S.3.2.3	• NRMMs should be approved or exempted with a label issued by EPD. The label should be displayed at a conspicuous position of the machine or vehicle. Nonroad vehicles are required to meet the Euro V emission standards and smoke requirements as stipulated under the Air Pollution Control (Vehicle Design Standards) (Emission) Regulation.	Emission from NRMM during Construction Phase	Contractor(s)	At all construction areas of the site during the entire construction period	Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation	Deficiency of Mitigation Measures but rectified by the Contractor.	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.3.8.1	S.3.2.3	• The works at overlapping section are recommended to be scheduled to avoid works at the areas near Fan Kam Road. • The Contractor shall liaise with No. CE 61/2012 (HY) – Improvement to Fan Kam Road – Investigation contractors so as to avoid undertaking works concurrently with the works from CE 61/2012 Project when they are in the close proximity. As a conservative approach, works for drainage improvement shall be carried when the works from the No. CE 61/2012 project is over 500 m away.	Prevent potential cumulative construction air quality impacts	Contractor(s)	At all construction areas of the site for Ha Che during the entire construction period	-	Implemented	HC: 20 Feb 2024

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Noise Impact – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
Construction Phase									
S.4.6.6	S. 4.8.1	Use of quiet PMEs and smaller sized of PMEs as practicable.	Noise control during construction	Contractor(s)	Construction areas near the specified locations during the construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	
S.4.6.7	S. 4.8.1	Use of quiet PME for generator, mobile crane and excavator, wheeled/ tracked.	Noise control during construction	Contractor(s)	Construction areas near the specified locations during the construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	
S.4.6.8	S. 4.8.1	The Contractor should be responsible for the design of temporary/ movable noise barriers with consideration of the size of PME and the requirements of intercepting the line of sight between the noise sensitive receivers and PME.	Noise control during construction	Contractor(s)	Construction areas near the specified locations during the construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	The mitigation measures of utilising material stockpiles and other structures as noise barriers, is not applicable to the construction areas.

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
S.4.7.1	S. 4.8.1	• The Contractor shall adopt the Code of Practice on Good Management Practice to Prevent Violation of the NCO (Cap. 400) (for Construction Industry) published by the EPD; • The Contractor shall observe and comply with the statutory and non-statutory requirements and guidelines; • Before commencing any work, the Contractor shall submit to the Environmental Review for approval the method of working, equipment and noise mitigation measures intended to be used at the site; • The Contractor shall devise and execute working methods to minimise the noise impact on the identified surrounding sensitive uses, and provide experienced personnel with suitable training to ensure that those methods are implemented; • Noisy equipment and noisy activities should be located as far away from the NSR's as is practical;	Noise control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
S.4.7.1	S. 4.8.1	• Machines and plant (such as dump truck, vibratory compactor, lorry, cranes) that may be intermitted use should be shut down between work periods or should be throttled down to a minimum. Additionally, the combined use of noisy equipment/ machines should be avoided, when possible; • Only well-maintained plant should be operated on-site and plants should be serviced regularly during the construction programme; • Silencers, mufflers or acoustic treatment mats on construction equipment should be utilised and properly maintained during the construction duration; • Plants known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and • Material stockpiles and other structures should be effectively utilised as noise barriers, where practicable.	Noise control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
S.4.7.2	S. 4.8.1	The Contractor shall, from time to time, be aware of the noise impacts on the surrounding NSRs through adequate noise monitoring during the works so that adjustments can be made to the number of plants used for any construction activity and the corresponding plant positioning. These requirements shall be incorporated into the project works contract.	Noise control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	EIAO-TM and NCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Ecological Impact – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
S.5.9.2	S.5.2.1	The section of watercourse with construction activities should be hydrologically isolated from the rest of the watercourse as far as practicable (except discharge of treated runoff).	Ecological – to avoid and minimize the spatial impact/ disturbance to the riverine habitat	Contractor(s)	During construction at all sites	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.5.9.2	S.5.2.1	The staged construction activities should be commenced from upstream and progresses toward the downstream area and the reinstatement work especially the planting of riparian vegetation should also be undertaken in stages and commenced as soon as the hardscape work completed in the working section	Ecological – to avoid and minimize the spatial impact and shorten the temporal disturbance to the riverine habitat	Contractor(s)	During construction at all sites	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.5.9.3	S.5.2.2	Good Site Practice • Effective implementation of an Environmental Management Systems in accordance with the ISO 14001 for all work sites; • Effective implementation of mitigation measures recommended for dust suppression, noise reduction, as well as water quality and waste management as detailed in other sections of the EIA Report.	Ecological – to avoid or minimize the potential disturbance to the habitats and wildlife inhabited within or adjacent to the work sites	Contractor(s)	During construction at all sites	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.5.9.3	S.5.2.2	• Effective implementation of the Tree Preservation Measures as detailed in the guidelines published by the Tree Management Office. • Staff awareness training on the ecological importance of the riverine habitats and inhabited wildlife, as well as briefing on the mitigation measures recommended in the EIA Report. • Well defined and fenced Work Area to prevent intentional or accidental encroachment or trespassing into the adjacent habitats for access, parking and operation of plants/ machineries, as well as stockpiling of construction material or waste; • Fence off any potentially ecologically sensitive resources within the work area with warning signpost; • Water diversion by means of submerged water pump should be avoided as far as practicable to prevent obstruction of wildlife movement along the channel; • Waste and refuse should be stored or dumped in appropriate receptacles and on-site burning of waste should be strictly prohibited; • Excavated material should be properly covered or promptly disposed of, and opportunities to stockpile and backfill the topsoil should be explored;	Ecological – to avoid or minimize the potential disturbance to the habitats and wildlife inhabited within or adjacent to the work sites	Contractor(s)	During construction at all sites	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.5.9.3	S.5.2.2	• No chemical should be stockpiled on-site until absolutely necessary; • On-site maintenance of plant/ machineries/ vehicle should be avoided as far as practicable; • Silt/ Sediment/ Oil traps should be installed to avoid direct discharge of effluent or site run-off; • Regular ecological checks; • Cut down of vegetation during site clearance should be in stages before groundwork takes place as such to disperse any wildlife that is sheltering in the immediate area; and • Minimise vehicle access.	Ecological – to avoid or minimize the potential disturbance to the habitats and wildlife inhabited within or adjacent to the work sites	Contractor(s)	During construction at all sites	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.5.9.4	S.5.2.10	The construction work in Tai Wo should be scheduled in the dry season and sandbags or other similar facilities should be placed along the southern boundary of the work site to prevent any accidental discharge of untreated effluent into the buffered grassland and EIS under adverse weather condition. In addition, discharge of any treated or untreated effluent, either by means of soakaway or direct discharge to nearby waterways, should be directed away from the grassland buffer and the EIS. The above measure should be audited regularly as part of the routine site inspection undertaken by the ET.	Ecological – to avoid and minimize any potential impact to the Cheung Po EIA from site discharge	Contractor(s)	Tai Wo	EIA, contractual requirements	Implemented	TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.5.9.6 to 5.9.7	S.5.2.7, 5.2.8	A detail survey to update the abundance and distribution of the endemic freshwater crabs within the project site (include the original watercourse which will be cut-off at Ha Che and Lin Fa Tei, inclusive of a receptor site search for the preparation of a "Freshwater Crab Translocation Plan", in which the whole process including logistic arrangement should be detailed for the approval of AFCD.	Ecological – to avoid/ minimize the direct impact to the local population of these two endemic freshwater crab species	Engineer	Lin Fa Tei and Ha Che, before the commencement of the construction work	EIA, contractual requirements	Implemented, EPD advised no comment on the FCTP on 9 Feb 2024. A formal reply letter was issued by the EPD on 4 July 2024 after the submission of hardcopy for their record.	HC: 20 Feb 2024 LFT: 20 Mar 2024
S.5.9.6 to 5.9.7	S.5.2.9	Capture and translocate two endemic freshwater crabs and undertake post-translocation monitoring programme in accordance to the approved "Freshwater Crab Translocation Plan".	Ecological – to avoid/ minimize the direct impact to the local population of these two endemic freshwater crab species.	Contractor, ET	Lin Fa Tei and Ha Che, within one month before the commencement of the construction work	EIA, contractual requirements	Implemented, pre-construction surveys at Ha Che and Lin Fa Tei were completed between 5 and 7 Feb 2024 and 11 and 13 Mar 2024 respectively	HC: 20 Feb 2024 LFT: 20 Mar 2024
S.5.9.6 to 5.9.8	S.5.2.9	Before the commencement of a construction work in a new section, the site should be inspected by the ecologist to confirm no inhabitation of the two freshwater crab species.	Ecological – to avoid/ minimize the direct impact to the local population of these two endemic freshwater crab species	Contractor, ET	Lin Fa Tei and Ha Che, within one month before the commencement of the construction work	EIA, contractual requirements	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.5.9.9	S.5.2.4	The *Aquilaria sinensis* (seedling) within the site boundary at Sung Shan New Village to be protected and retained during construction in accordance with DEVB TCW No. 4/2020 Tree Preservation	Ecological – to preserve the floral species of conservation concern	Engineer	Sung Shan New Village	EIA, contractual requirements	Implemented	SSNV: 16 Apr 2024
S.5.9.13-5.9.19	S.5.2.15	Restoration of wildlife habitat by ecological habitat and niche that could promote colonisation of aquatic wildlife during the reinstatement of embankment and channel bed	Ecological – to compensate for the loss of wildlife habitat especially the two endemic freshwater crab species	Contractor(s)	All sites during construction	EIA, contractual requirements	The restoration and planting works will be conducted after the completion of construction work at Ha Che, Lin Fa Tei and Sung Shan New Village	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Water Quality Impact – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
Construction Phase									
S.6.7.2	S.6.2.3	The mitigation measures should cover, but not limited to the following Best Management Practices: • Sand/ silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove sand/ silt particles from runoff to meet the requirements of the Technical Memorandum standards under the WPCO. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 2/23. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. • Work programmes should be designed to minimize the size of work areas to minimize the soil exposure soil and reduce the potential for increased siltation and runoff; • Silt removal facilities, channels and manholes should be	Water quality control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO and ProPECC PN 2/23	Deficiency of Mitigation Measures but rectified by the Contractor.	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	WPCO licenses for HC, LFT, SSNV and TW were granted on 26 Apr 2024, 24 May 2024, 10 July 2024 and 29 July 2024 respectively.

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		maintained and cleaned regularly to ensure the proper function; • Water pumped out from excavations should be discharged into silt removal facilities; • Careful programming of the works to minimize soil excavation during the rainy season. If excavation of soil cannot be avoided during the wet season (April to September), exposed slope surfaces should be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarized in ProPECC PN 2/23; • Earthwork surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed; • Wastewater generated from the washing down of mixer trucks and drum mixers and similar equipment should wherever practicable be recycled. The							

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		discharge of wastewater should be kept to a minimum; • To prevent pollution from wastewater overflow, the pump sump of any water recycling system should be provided with an on-line standby pump of adequate capacity and with automatic alternating devices; • Under normal circumstances, surplus wastewater may be discharged into foul sewers after treatment in silt removal and pH adjustment facilities (to within the pH range of 6 to 10). Disposal of wastewater into storm drains will require more elaborate treatment. Surface run-off should be segregated from the concrete batching plant and casting yard area as much as possible, and diverted to the stormwater drainage system. Surface run-off contaminated by materials in a concrete batching plant or casting yard should be adequately treated before disposal into stormwater drains; • Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric during rainstorms.							

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
S.6.7.4	S6.2.3	The guidelines stipulated in the ProPECC PN 2/23 "Construction Site Drainage" issued by the EPD should be followed to minimise the potential water quality impacts. Good housekeeping and stormwater best management practices, as detailed below, should be implemented to ensure that all construction runoff are well controlled to minimise the water quality impacts that arise due to the construction works of the Project. • Flood protection such as dikes or embankments should be provided around the boundaries of earthwork areas. Temporary ditches should be provided as appropriate to facilitate the runoff discharge into drainage system, through a silt/ sediment trap. The silt/ sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates; • Construction works should be programmed to avoid surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible	Water quality control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO and ProPECC PN 2/23	Deficiency of Mitigation Measures but rectified by the Contractor.	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	• WPCO licenses for HC, LFT, SSNV and TW were granted on 26 Apr 2024, 24 May 2024, 10 July 2024 and 29 July 2024 respectively. • The provision of oil interceptors in the drainage system downstream is not applicable as there is no oil/ fuel pollution spotted at the construction sites. • Fuel tanks and storage areas are not placed

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means; • All drainage facilities and erosion and sediment control structures, if any, should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms; • Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas; • All open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system; 3Manholes (including newly constructed ones) should							

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers; • Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 2/23. Particular attention should be paid to the control of silty surface runoff during storm events; • All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access							

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		road leading to, and exiting from, the wheel-washing bay to the public road should be paved with sufficient backfall toward the wheel-washing bay to prevent vehicle tracking of soil and silty water to public roads and drains; • Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources as far as possible. The oil interceptors, if any, should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage; • Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts; • All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby.						

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
S.6.7.5	S.6.2.3	Maintenance of vehicles and equipment involving activities with potential for leakage and spillage is expected to be carried out off-site and should only be undertaken within areas appropriately equipped to control these discharges.	To control the effluent discharge during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	
S.6.7.6	S.6.2.3	Contractor shall apply for a discharge license under WPCO.	To control the effluent discharge during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO	Implemented.	HC: 26 Apr 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	
S.6.7.7 & S.6.7.8	S.6.2.3	Sewage from Workforce • Portable chemical toilets and/ or sewage holding tanks should be provided for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets to cater to 0.15 m^3/day/worker of sewage and be responsible for appropriate disposal and maintenance. • Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the	To control sewage generation during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO and Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		construction phase of the project. Regular environmental audit on the construction site should be conducted to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the project would not cause water quality impact after undertaking all required measures.							
S.6.7.10 - S.6.7.15	S.6.2.3	Widening of Drainage Channels • Due to the characteristics of narrow width and small water flow of the existing channel, the excavation should be carried out in dry condition (even in wet season) by diverting the stream flow from upstream by a temporary drainage channel with a temporary sheet piles, earth bund or barrier so that the works area will remain dry for later excavation and widening works; • The temporary drainage channel would be backfilled when the construction works are completed or the temporary	Water quality control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		diversion is no longer required. Although flooding of the proposed contaminant section seldom occurs in dry season, the excavation would consider to suspend when flood water enters the containment causing leakage of runoffs to stream water; • After dewatering of the streams, the sediments should be allowed to dry before excavation (yet still maintain a moist state to avoid dust nuisance). This will facilitate excavation of the sediments and also minimize the risk of drained water flowing back into watercourses or diversion channels as the sediment is handled. Where time or weather constraints require handling of wet sediment, care should be taken in the removal of sediment and the storage area should be bunded to prevent silty runoff entering watercourses. Given its small quantity, all excavated sediment should be reused on-site as backfilling material; • To further minimize the leakage and loss of sediments during excavation, tightly sealed closed							

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		grab excavators should be employed in river sections where material to be handled is wet. Where material is dry and in non-river sections, conventional excavations can be used; • Excavated sediment will likely be temporarily stored on-site for reuse as backfilling material. This should be stored in a bunded area and covered at any time to avoid inadvertent release of silts and suspended solids to nearby water bodies; • Regular monitoring of suspended solids, pH and turbidity should be conducted during excavation works. Any exceedance of water quality in the nearby water bodies caused by inadvertent release of site runoff should be rectified in accordance with EM&A programme for this project.							
S.6.7.16	S6.2.3	Cast in-situ Construction • Minimise the area of the site which generates contaminated stormwater runoff; • Provide a separate dedicated drainage system to discharge clean stormwater from the site;	Water quality control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		• Drain all contaminated stormwater and process wastewater to a collection pit for recycling; • Regularly clean out solids that accumulate in the pit; • There must be no dry weather wastewater discharges from the site; • Monitor wet weather discharges for pH and suspended solids. Retain the records.							
S.6.7.17	S6.2.3	Registration to EPD as a CWP (Chemical Waste Producers) is required if chemical wastes are generated and need to be disposed of. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance (WDO). The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the WDO should be used as a guideline for handing chemical wastes.	Water quality control during construction	Contractor(s)	At all construction areas of the site during the entire construction period	WPCO, WDO and the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024	
S.6.7.18	S.6.2.3	Mitigation measures to avoid potential impact to Cheung Po EIS • The construction work in Tai Wo should be scheduled in the dry season and sand bags or other similar facilities should be	Water quality control during construction	Contractor(s)	At Tai Wo Area during the entire construction period	WPCO	Implemented	TW: 16 Dec 2024	

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation	Remarks
		placed along the southern boundary to the work site to prevent any accidental discharge of untreated effluent into the buffered grassland and EIS under adverse weather condition; • Discharge of any treated or untreated effluent, either by means of soakaway or direct discharge to nearby waterways, should be directed away from the grassland buffer and the EIS.							

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Waste Management Implication – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
S.7.5.1	S.7.2.5	• An on-site environmental co-ordinator employed by the contractor should be identified prior to the outset of the work. Prior to commencement of project, the environmental coordinator shall prepare a WMP in accordance with the requirements set out in the ETWB TCW No. 19/2005, Waste Management on Construction Sites, for the Engineers Representative's approval. The WMP shall include monthly and yearly Waste Flow Tables (WFT) that indicate the amount of waste generated, recycled and disposed of (including final disposal location), and which should be regularly updated;	Waste management during construction	Contractor(s)	Prior to commencement of Project works and implemented throughout the entire construction period	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• The Project contractor's waste management practices and effectiveness should also be audited by the Engineer on a regular basis;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• The reuse/ recycling of all materials on site should be investigated and exhausted prior to treatment/ disposal off-site;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.7.5.1	S.7.2.5	• Good site practices should be adopted from the commencement of works to avoid the generation of waste, reduce cross contamination of waste and to promote waste minimisation;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• All waste materials should be sorted on-site into inert and non-inert C&D materials, and where the materials can be recycled or reused, they should be further segregated. Inert material, or public fill will comprise stone, rock, masonry, brick, concrete and soil which is suitable for land reclamation and site formation whilst non-inert materials include all other wastes generated from the construction process such as plastic packaging and vegetation;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.7.5.1	S.7.2.5	• The Project contractor should be responsible for identifying what materials can be recycled/ reused, whether on-site or off-site. In the event of the latter, the contractor should make arrangements for the collection of the recyclable materials. Any remaining non-inert waste should be collected and disposed of to the landfill as last resort whilst any inert C&D materials should be re-used on site as far as possible. Alternatively, if no use of the inert materials can be found on-site, the materials can be delivered to a public fill area or public fill bank after obtaining the appropriate licence;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• In order to monitor the disposal of C&D materials and solid waste at public filling facilities and landfills, and to control fly-tipping, a trip ticket system shall be implemented by the contractor, in accordance with the contract and the requirements of DEVB TCW No. 6/2010 “Trip Ticket System for Disposal of Construction and Demolition Material”;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	DEVB TCW No. 6/2010	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.7.5.1	S.7.2.5	• Under the Waste Disposal (Chemical Waste) (General) Regulation, the Project contractor shall register as a Chemical Waste Producer (CWP) if chemical wastes such as spent lubricants, paints, etc. are generated onsite. Only licensed chemical waste collectors shall be employed to collect any chemical waste generated onsite. The handling, storage, transportation and disposal of chemical wastes shall be conducted in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes and A Guide to the Chemical Waste Control Scheme both published by the EPD;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	Waste Disposal (Chemical Waste) (General) Regulation	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• A sufficient number of covered bins should be provided onsite for the containment of general refuse to prevent visual impacts and nuisance to the sensitive surroundings. These bins should be cleared daily and the collected waste disposed of to the nearest refuse transfer station. Further to the issue of DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness, the contractor is required to maintain a clean and hygienic site throughout the Project works;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction period	Waste Disposal Ordinance and DEVB TC(W) No. 8/2010	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.7.5.1	S.7.2.5	• Minimize windblown litter and dust during transportation by either fitting trucks with mechanical covers or transporting waste in enclosed containers;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• All chemical toilets, if any, should be regularly cleaned and the night-soil collected and transported by a licensed contractor to a Government Sewage Treatment Works facility for disposal;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• Toolbox talks should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling; and	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	• The project contractor shall comply with all relevant statutory requirements and guidelines and their updated versions that may be issued during the course of the project construction.	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	Waste Disposal Ordinance	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S.7.5.1	S.7.2.5	Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. • Segregation and storage different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S.7.5.1	S.7.2.5	• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the workforce; • Use of reusable non-timber formwork to reduce the amount of C&D material; • Prior to disposal of C&D waste, it is recommended that wood, steel and other metal shall be separated for re-used and/ or recycling to minimise the quantity of waste to be disposal of to landfill; • Proper storage and site practice to minimise the potential for damage and contamination of construction materials; • Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	Waste management during construction	Contractor(s)	At all construction areas of the site during the entire construction	ETWB TCW No. 19/2005	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Land Contamination – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
S.8.8.1	S.8.2.1	Unexpected contaminated materials may be encountered near identified potential contaminated sites during construction. Should suspected contamination be found during construction, the extent and nature of contamination within project areas should be properly assessed and the contaminated soil/ groundwater should be remediated in accordance with EPD issued publications as below: • Guidance Note for Contaminated Land Assessment and Remediation; • Guidance Manual for Use of Risk-based Remediation Goals (“RBRGs”) for Contaminated Land Management; and • Practice Guide for Investigation and Remediation of Contaminated Land.	Safety precautionary measures for handling possible contaminated materials	Contractor(s)	During construction works within the works areas nearby the land contamination sites HC-A, HC-C, HC-D, HC-I, LFT-A, LFT-B, LFT-C, LFT-D, LFT-E and SSNV-A	Guidance Note for Contaminated Land Assessment and Practice Guide for Investigation Remediation of Contaminated Land	No unexpected contaminated material was encountered during reporting period	N/A

Landscape & Visual Impact – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
S9.12.1.1	S.9.2	Construction Site Control CM01 - Tree Protection and Preservation Trees / woodland within the Project Site which are unaffected by the works shall be protected and preserved during the construction phase. The tree preservation proposals shall be coordinated with the layout and design of the engineering and architectural works at detailed design stage for further retention of individual trees.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM02 – Compensatory Tree Planting If removal of trees unavoidable due to construction impacts, trees will be compensated where technically feasible.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	No tree was removed during reporting period	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM03 - Works Area and Temporary Works Areas (Good Site Practice) The construction sequence and construction programme shall be optimized in order to minimize the duration of impact. Construction site controls shall be enforced including the storage of materials, and the location and appearance of site accommodation and site storage. The site office or temporary above-ground structures shall be sited in locations which are not visually prominent.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S9.12.1.1	S.9.2	CM04 - Advance Implementation of Mitigation Planting Replanting of existing/ disturbed vegetation shall be undertaken as soon as technically feasible.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	No replanting work was conducted during reporting period	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM05 - Coordination with Concurrent Projects Coordinated implementation programme with concurrent projects to minimise impacts and where possible reduce the period of disturbance.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM06 - Decorative Screen Hoarding Decorative screen hoarding will be erected along areas of the construction works site boundary where the works site borders publicly accessible routes and/ or is close to visually sensitive receivers (VSRs) to screen undesirable views of the works site. It is proposed that the screening be compatible with the surrounding environment and where possible, non-reflective, recessive colours be used.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM07 – Light Control Construction and night time lighting glare will be controlled to minimize glare impact to adjacent VSRs during the construction stage. This is considered a general measure for good practice.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
S9.12.1.1	S.9.2	CM08 – Topsoil reuse Excavated topsoil should be conserved for re-use by the project or other projects. This is considered a general measure for good site practice.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024
S9.12.1.1	S.9.2	CM09 - Channel Bed Translocation Excavated natural stream bedding should be conserved for re-use by the project. This is considered a general measure for promoting sustainability and ecological continuity.	Good site practices and to minimize landscape and visual impact	DSD and its contractors.	Work sites	EIAO-TM	Implemented	HC: 20 Feb 2024 LFT: 20 Mar 2024 SSNV: 16 Apr 2024 TW: 16 Dec 2024

Remarks:
1. “HC” equal to Ha Che
2. “LFT” equal to Lin Fa Tei
3. “SSNV” equal to Sung Shan New Village
4. “TW” equal to Tai Wo

Cultural Heritage Impact – Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Construction Phase								
Table 10-3	Table 10.1	Lee Tat Bridge (GB-01) • A condition survey will be carried out in advance of works that may be affected by ground-borne vibration. The Condition Survey Report should contain descriptions of the structure, identification of fragile elements, an appraisal of the condition and working methods for any proposed monitoring and precautionary measures that are recommended with aid of photo records. The condition survey report must be submitted to AMO for comment before construction activities commence. The contractor should implement the approved monitoring and precautionary measures;	Cultural heritage protection	Contractors	During the construction period, for Lee Tat Bridge (GB-01)	AMO Guidelines on CHIA; EIAO-TM	The condition survey report was submitted on 22 Dec 2023. Antiquities and Monuments Office (AMO) had no adverse comment on the report on 3 Jan 2024. A formal reply letter was issued by the EPD on 21 Jun 2024 for their acceptance on the report.	N/A

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Table 10-3	Table 10.1	• Vibration monitoring should be undertaken during the construction works to ensure that safe levels of vibration are not exceeded. An Alert, Alarm and Action (AAA) vibration limit set at 5 / 6 / 7.5 mm/s for Grade 3 historic buildings should be adopted. A monitoring schedule, the location of monitoring equipment, the frequency of monitoring, reporting requirements and action plan should be included in the condition survey report. • The location of any monitoring equipment in the building must be approved by the owner before installation; • A buffer zone should be provided to separate the building or walls of the building from the construction works. The buffer zone should be clearly marked out by temporary fencing. The buffer zone should be made at least 5 m from the proposed works or if this is not possible as large as the site restrictions allow; • The contractor should ensure that safe public access is possible, through provision of clearly marked paths separated from the construction works areas, and is provided for any such affected cultural heritage structure. It is recommended that safe public access to the bridge be provided during the construction works.	Cultural heritage protection	Contractors	During the construction period, for Lee Tat Bridge (GB-01)	AMO Guidelines on CHIA; EIAO-TM	The condition survey report was submitted on 22 Dec 2023. Antiquities and Monuments Office (AMO) had no adverse comment on the report on 3 Jan 2024. A formal reply letter was issued by the EPD on 21 Jun 2024 for their acceptance on the report.	N/A

EIA Ref.	EM&A Ref.	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Who to implement the measures?	Location/ Timing of implementation of Measures	What requirements or standards for the measures to achieve?	Implementation Status	Starting date of Implementation
Table 10-3	Table 10.1	Lan Fong Study Hall (GB-02) • No mitigation required	N/A	N/A	N/A	AMO Guidelines on CHIA; EIAO-TM	N/A	N/A
Table 10-3	Table 10.1	St. John's Chapel (GB-03) • No mitigation required	N/A	N/A	N/A	AMO Guidelines on CHIA; EIAO-TM	N/A	N/A
Table 10-1	S.10.2.1 – S.10.2.2	• The proposed drainage works in the Lin Fa Tei area near previous wooden archaeological remains; • Archaeological survey prior to construction works in area marked on Figure 10.16 of the EIA report; • A qualified archaeologist shall apply for a licence under the Antiquities and Monuments Ordinance (Cap. 53) for the archaeological fieldwork.	Identification of archaeological remains, deposits and material within survey area Identification of archaeological extent	Qualified archaeologist engaged by Contractor	Prior to construction phase	Antiquities and Monuments Ordinance	The Archaeological Survey at Lin Fa Tei was carried out from 16 to 28 Oct 2024.	16 Oct 2024
Table 10-1	S.10.2.3	As a precautionary measure, the Antiquities and Monuments Office (AMO) should be informed immediately in case of discovery of antiquities or supposed antiquities in the course of excavation for the proposed drainage improvement works at Tai Wo area, Ha Che River area, Lin Fa Tei area (all areas except area identified for Archaeological Survey) and Sung Shan New village area, so that appropriate mitigation measures, if needed, can be timely formulated and implemented in agreement with AMO.	To ensure appropriate mitigation measures can be timely formulated and implemented to preserve archaeological data, if discovered, in agreement with AMO	Contractor	During construction phase	Antiquities and Monuments Ordinance	No antiquities or supposed antiquities was discovered during the reporting period	N/A

Remarks:
1. "HC" equal to Ha Che
2. "LFT" equal to Lin Fa Tei
3. "SSNV" equal to Sung Shan New Village
4. "TW" equal to Tai Wo

Appendix 2.1 Event and Action Plans for Water Quality

Event and Action Plan for Water Quality

Event	Action			
	ET [1]	IEC [1]	ER [1]	Contractor
Action Level being exceeded by one sampling day	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform the IEC and the Contractor; 4. Check monitoring data, all plant, equipment and the Contractor's working methods; 5. Discuss mitigation measures with the IEC and the Contractor; 6. Repeat measurement on next day of exceedance.	1. Discuss with the ET and the Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by the Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with the IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with the ET and the IEC and propose mitigation measures to the IEC and the ER; 6. Implement the agreed mitigation measures.
Action Level being exceeded by more than one consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform the IEC and the Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with the IEC and the Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; 8. Repeat measurement on next day of exceedance.	1. Discuss with the ET and the Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by the Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with the IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with the ET and the IEC and propose mitigation measures to the IEC and the ER within 3 working days; 6. Implement the agreed mitigation measures.

Event	Action			
	ET [1]	IEC [1]	ER [1]	Contractor
Limit Level being exceeded by one sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform the IEC, the Contractor and the DEP; 4. Check monitoring data, all plant, equipment and the Contractor's working methods; 5. Discuss mitigation measures with the IEC, the ER and the Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level.	1. Discuss with the ET and the Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by the Contractor and advise the ER accordingly; 3. Access the effectiveness of the implemented mitigation measures.	1. Discuss with the IEC, the ET and the Contractor on the proposed mitigation measures; 2. Request the Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with the ET, the IEC and the ER and propose mitigation measures to the IEC and the ER within 3 working days; 6. Implement the agreed mitigation measures.


Event	Action			
	ET [1]	IEC [1]	ER [1]	Contractor
Limit Level being exceeded by more than one consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact. 3. Inform the IEC, the Contractor and the DEP; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with the IEC, the ER and the Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days.	1. Discuss with the ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by the Contractor and advise the ER accordingly; 3. Access the effectiveness of the implemented mitigation measures.	1. Discuss with the IEC, the ET and the Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works until no exceedance of Limit Level.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with the ET, the IEC and the ER and propose mitigation measures to the IEC and the ER within 3 working days; 6. Implement the agreed mitigation measures; 7. As directed by the ER, slow down or stop all or part of the construction activities.


Note (1) ET – Environmental Team, IEC – Independent Environmental Checker, ER – Engineer's Representative, DEP – Director of Environmental Protection.


Appendix 2.2 Graphical Presentation of Water Quality Monitoring


Contract No. DC/2022/02
Drainage Improvement Works at Yuen Long -
Sung Shan New Village, Tai Wo, Lin Fa Tei and Ha Che
Water Quality Monitoring Result

Monitoring Location: C10

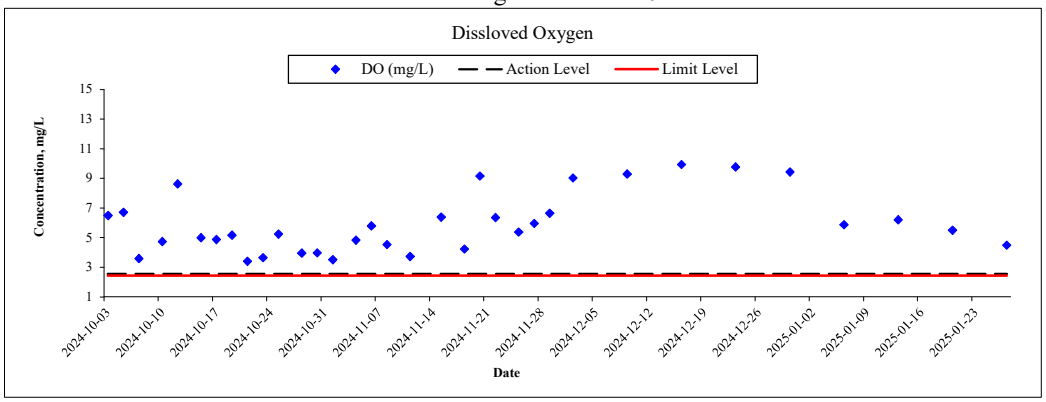


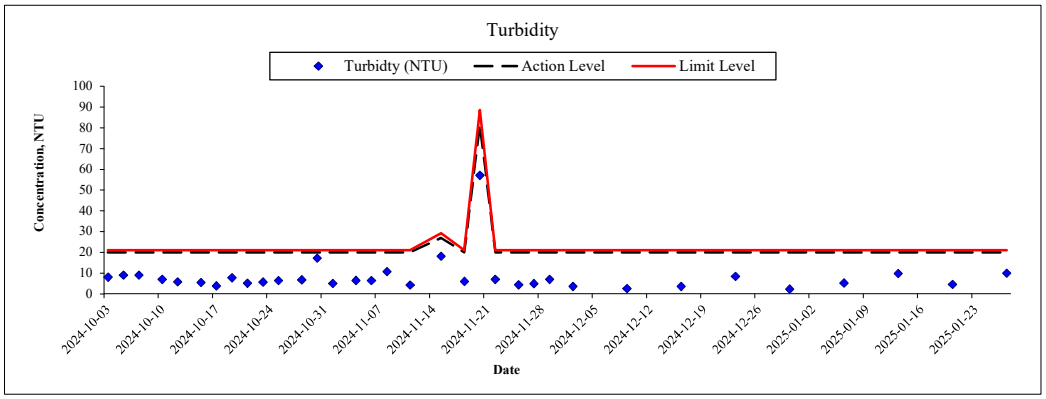


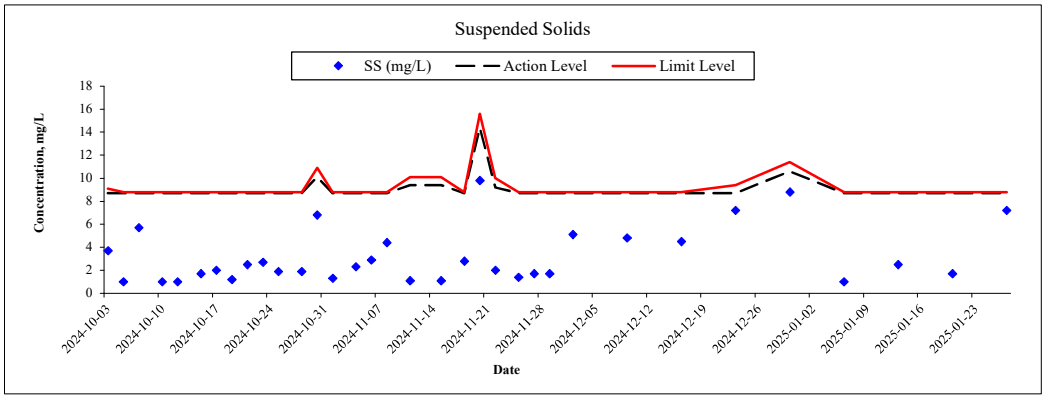


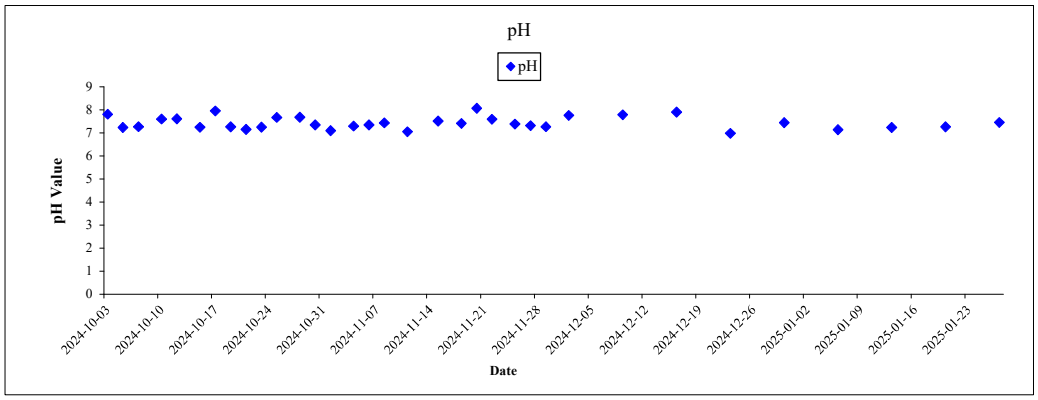


Monitoring Location: C9

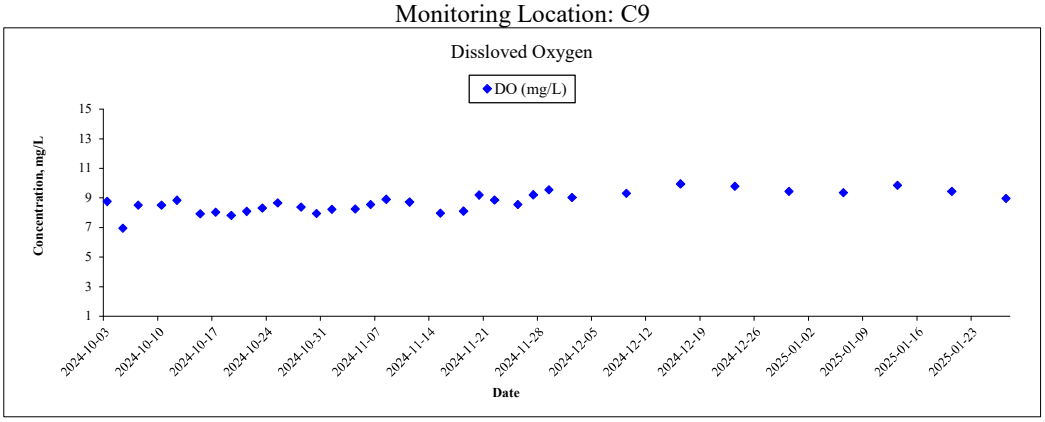


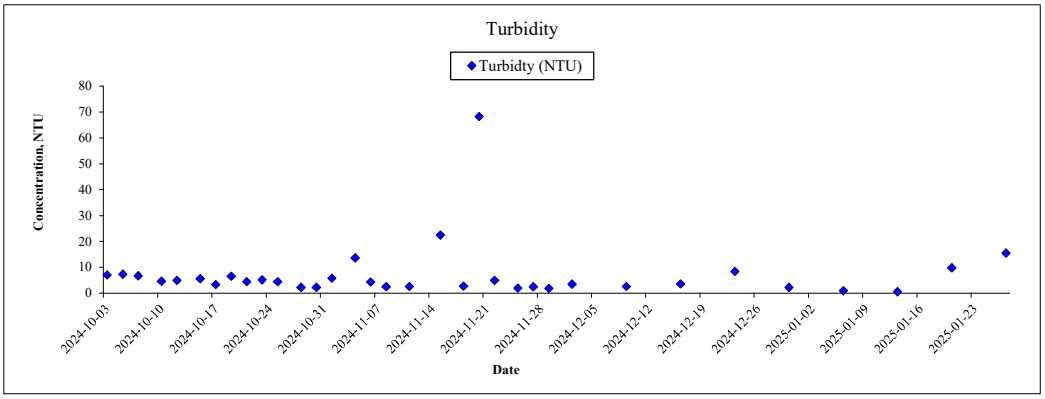


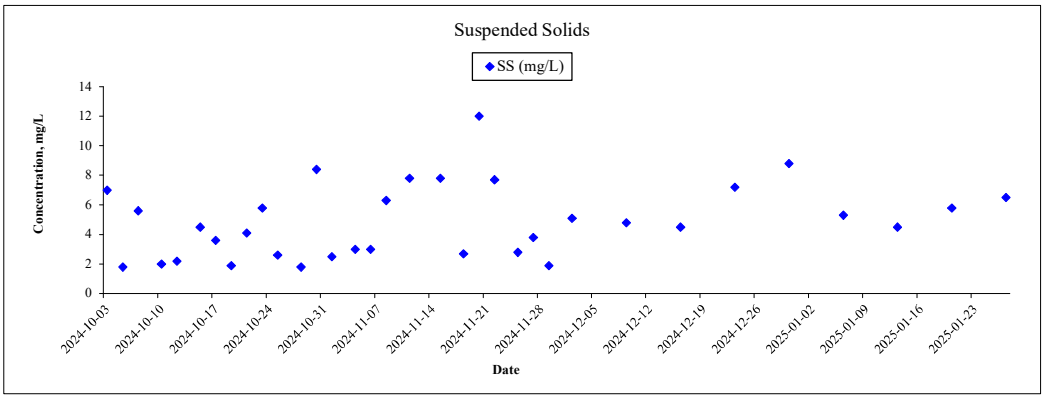


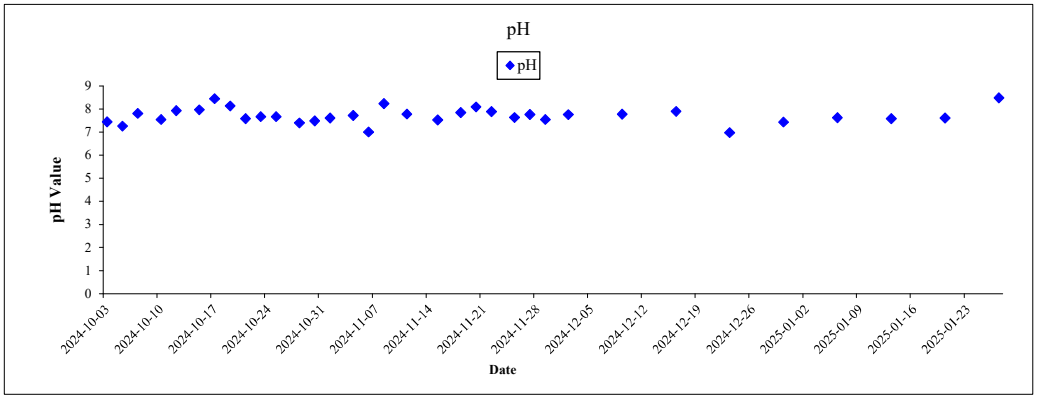


Monitoring Location: C8

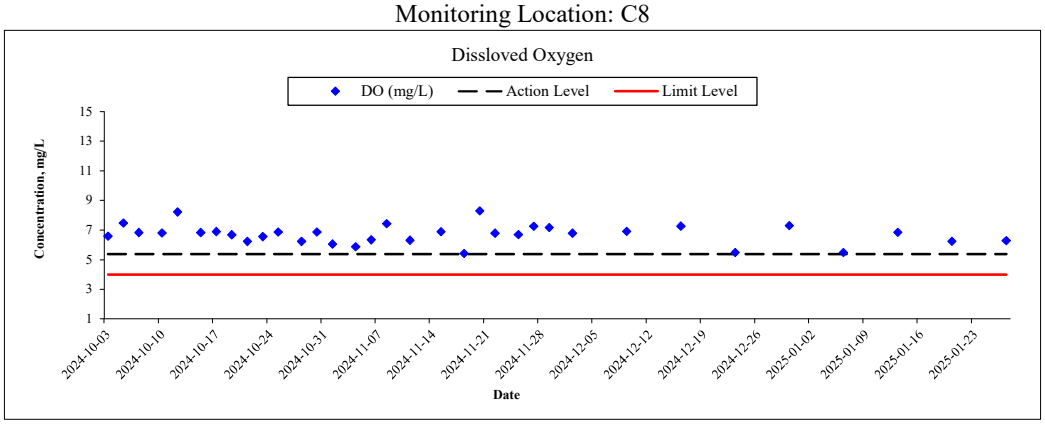


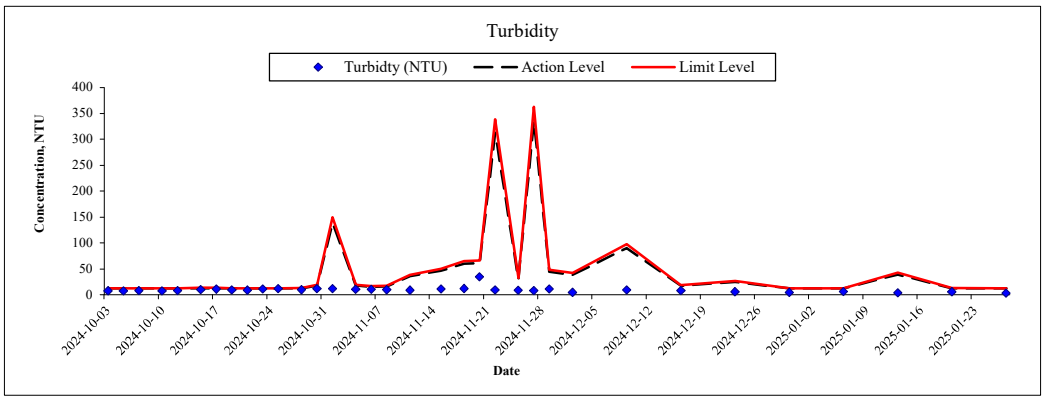


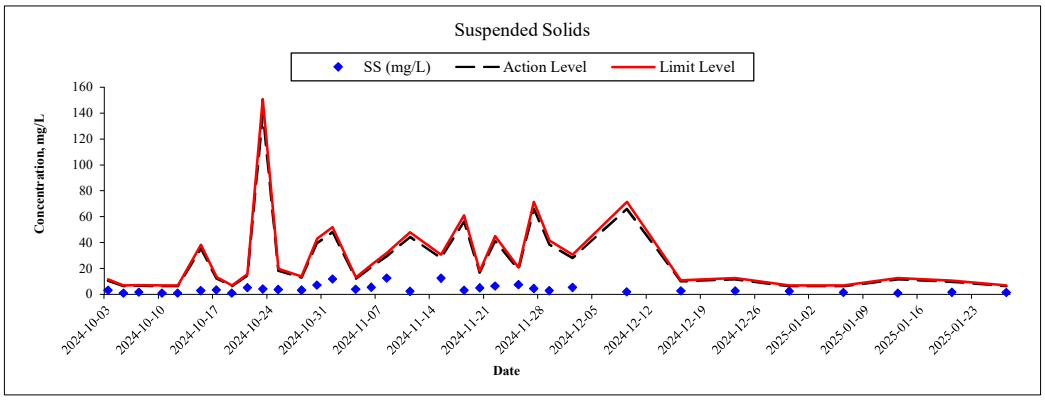


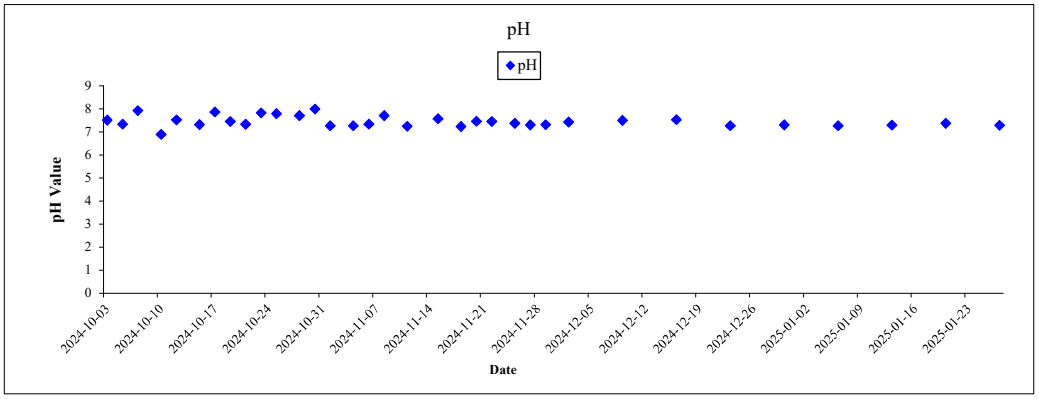


Monitoring Location: C7A

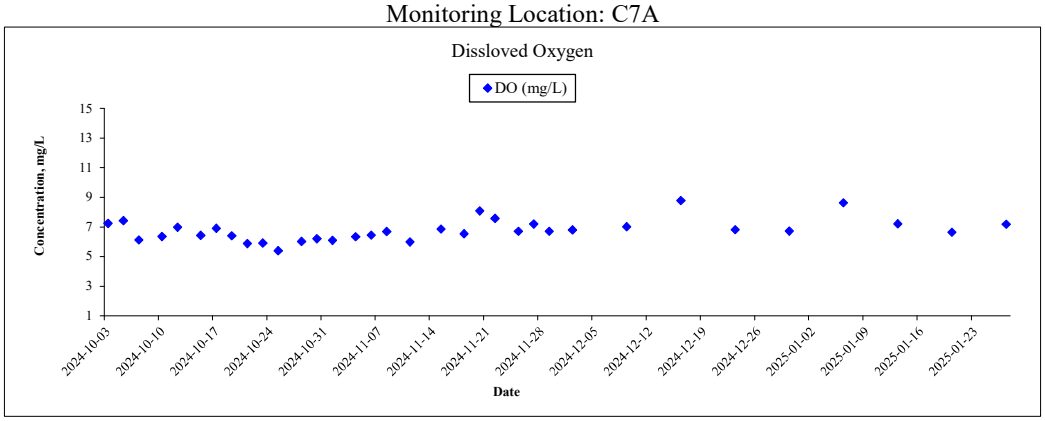


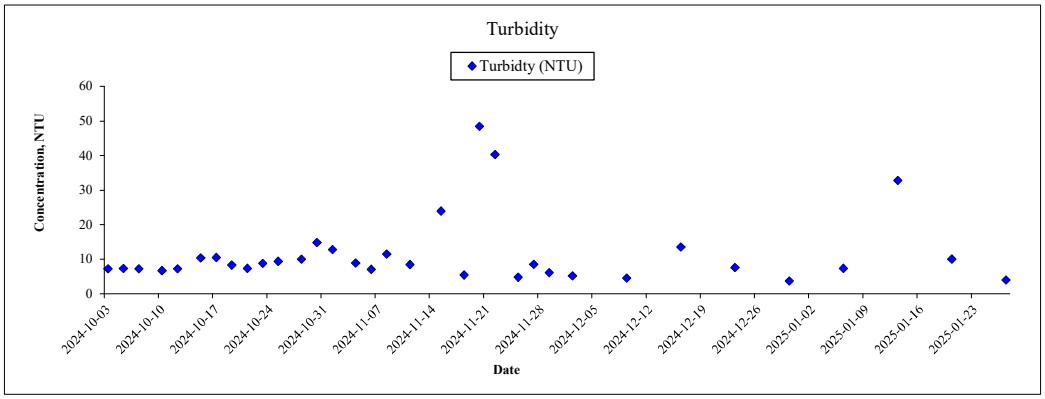


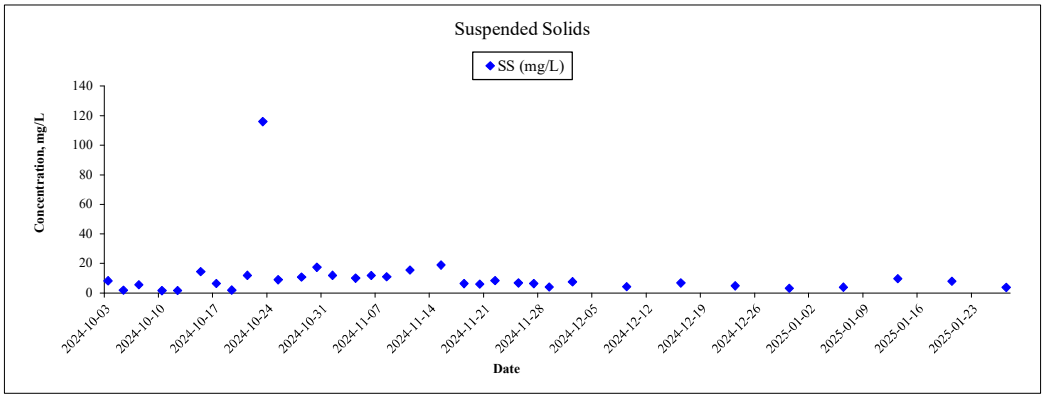


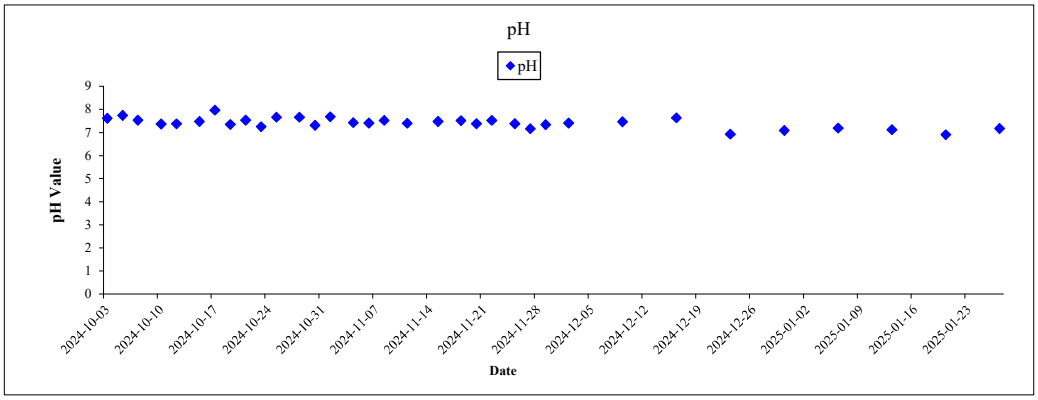


Monitoring Location: C6

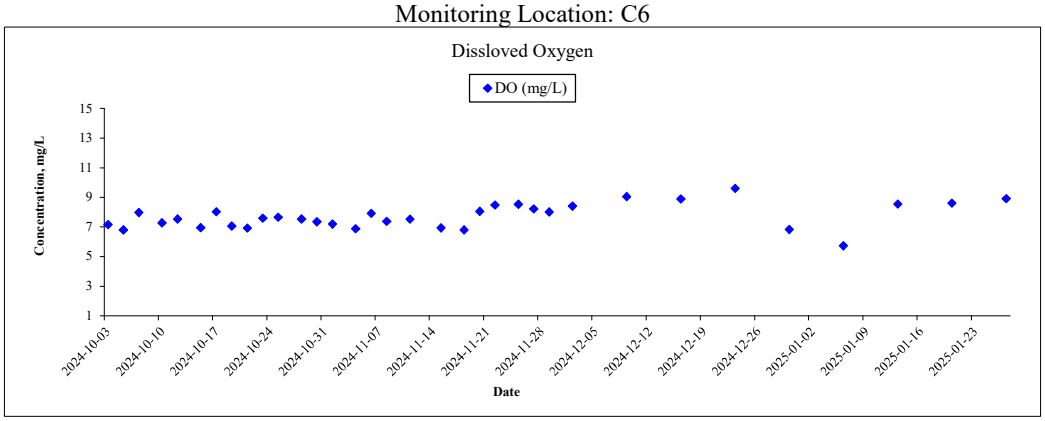


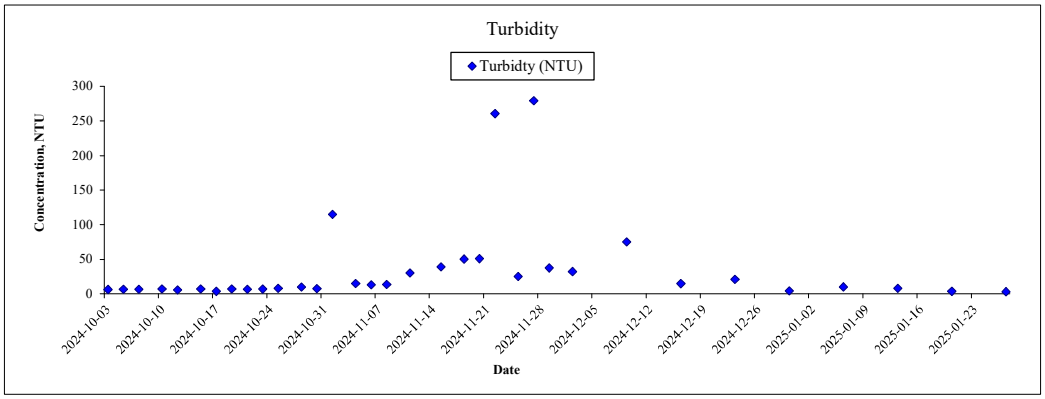


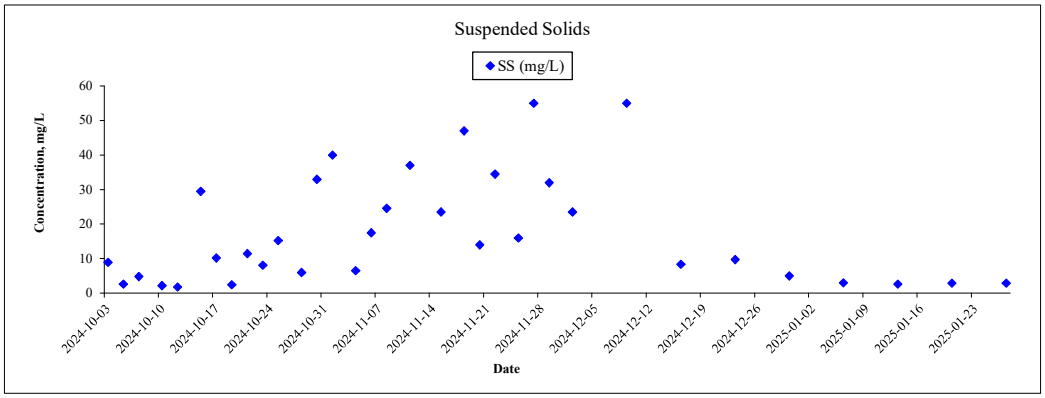


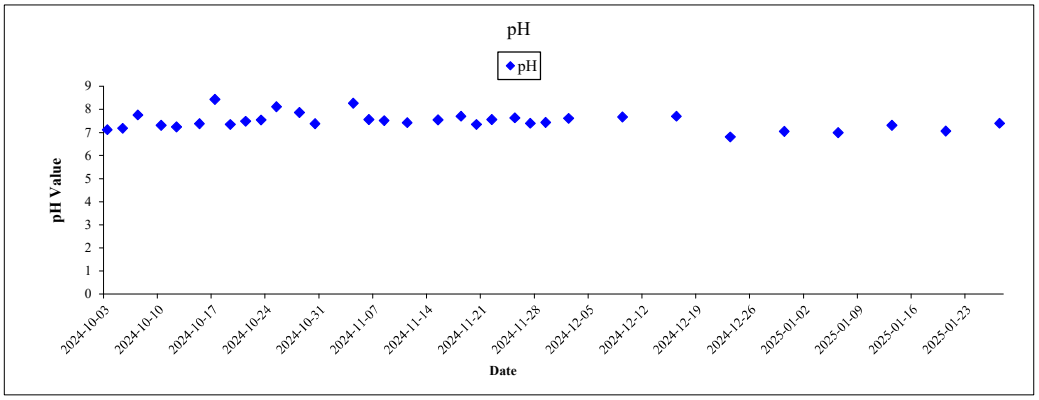


Monitoring Location: C5

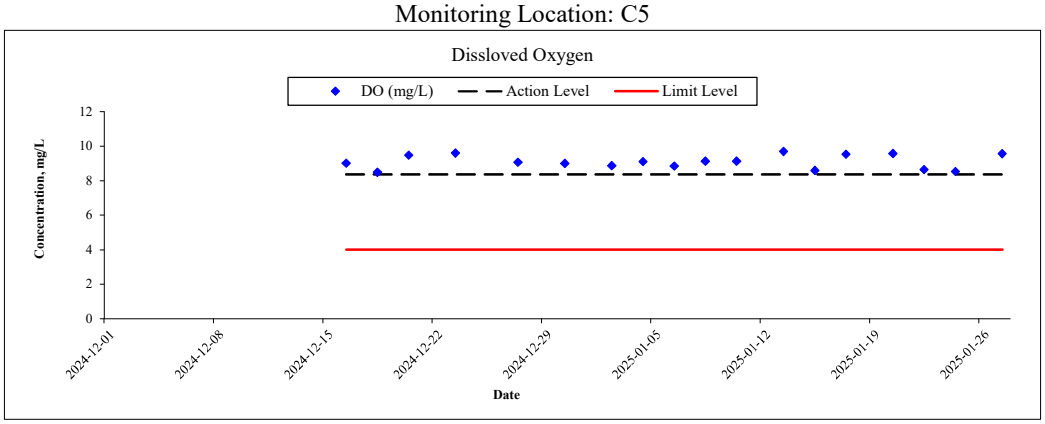


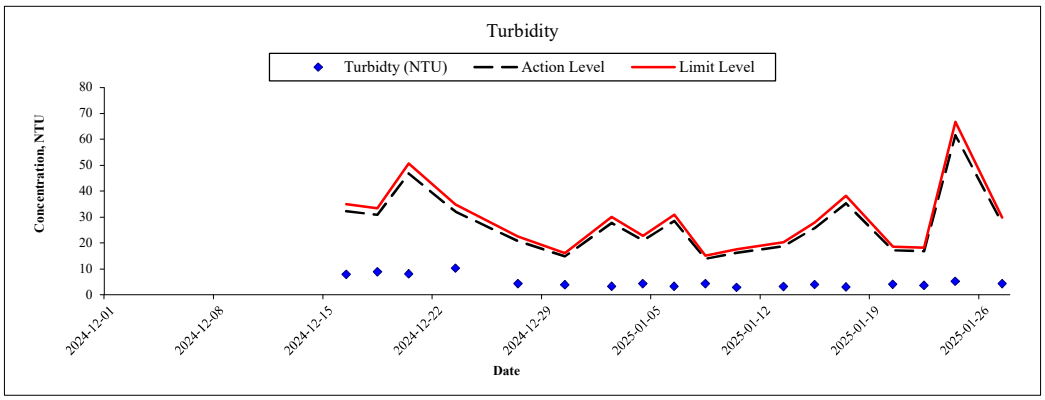


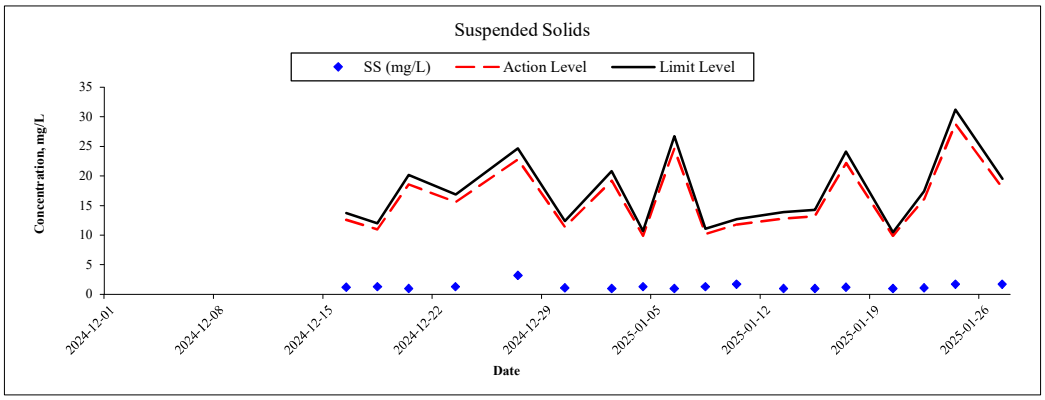


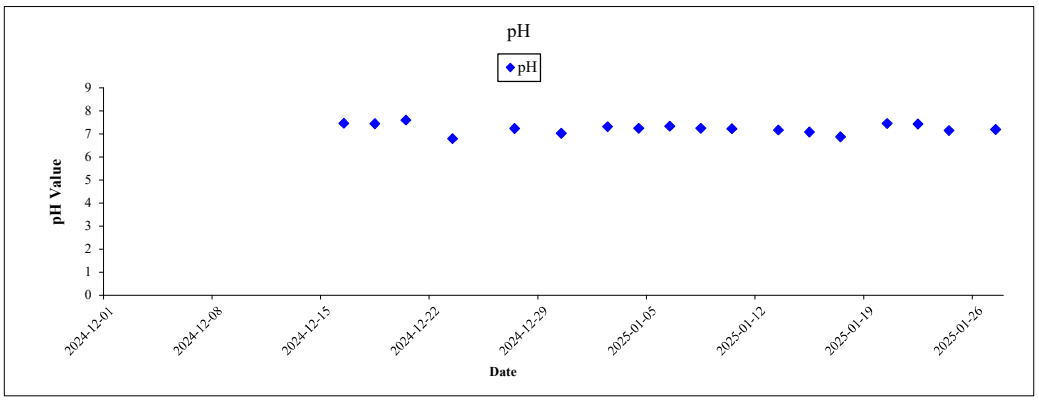


Monitoring Location: C4

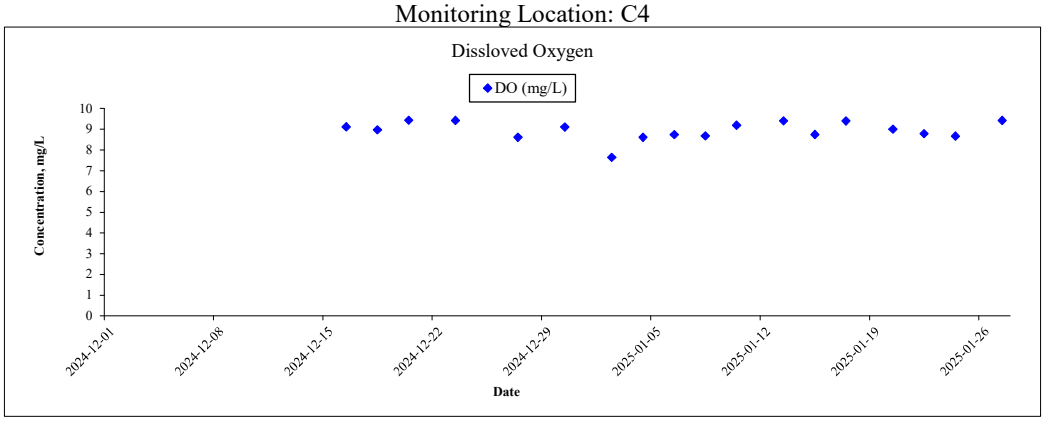


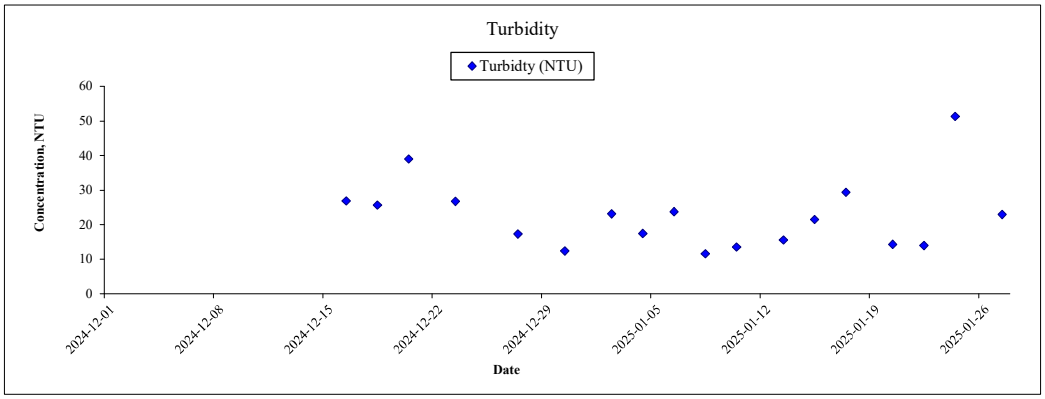


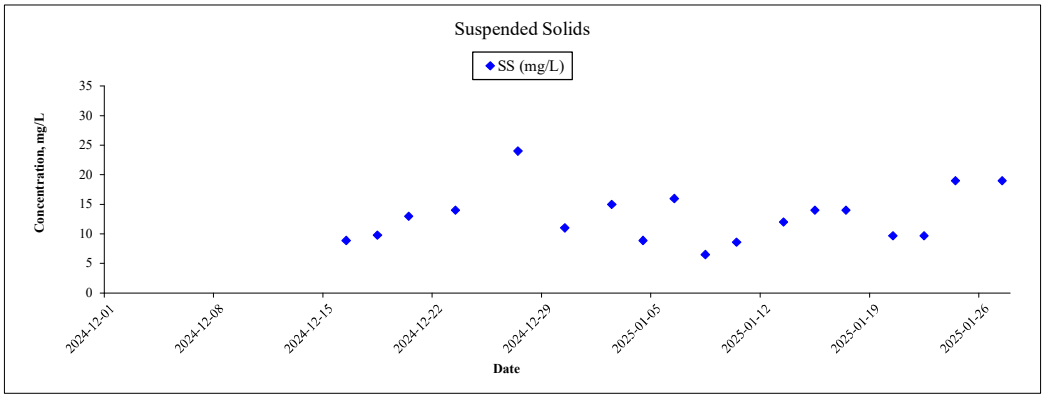


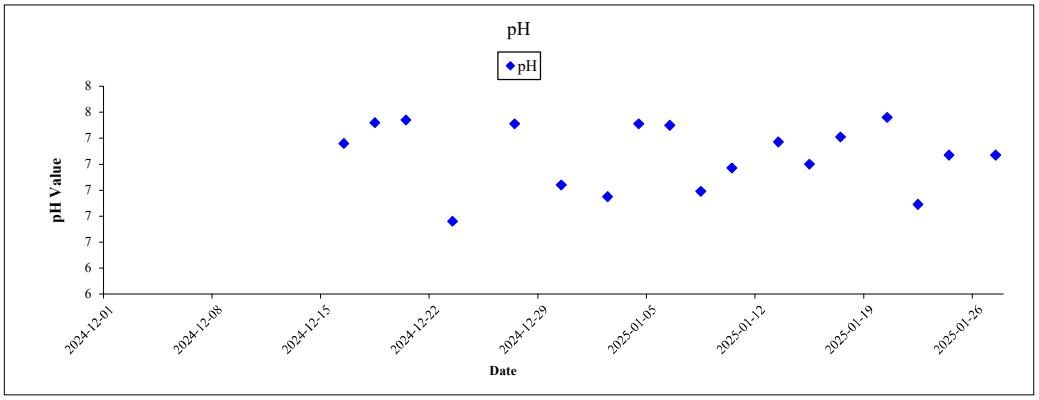


Monitoring Location: C3A

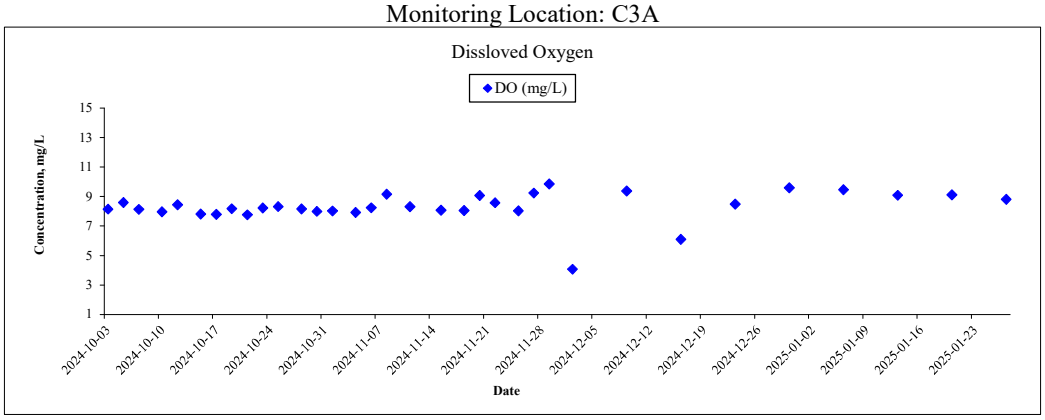


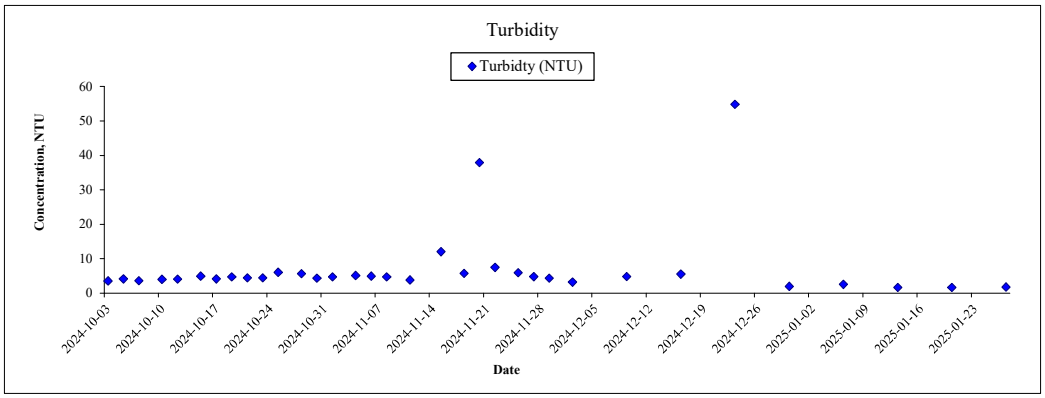


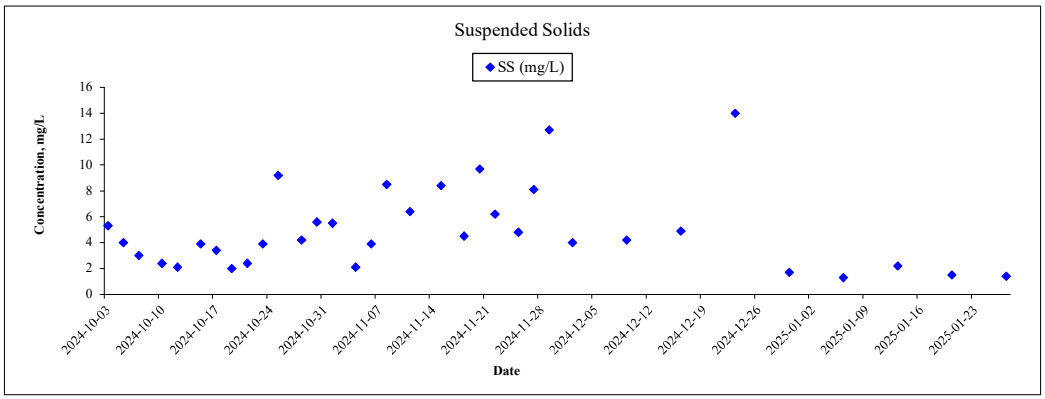


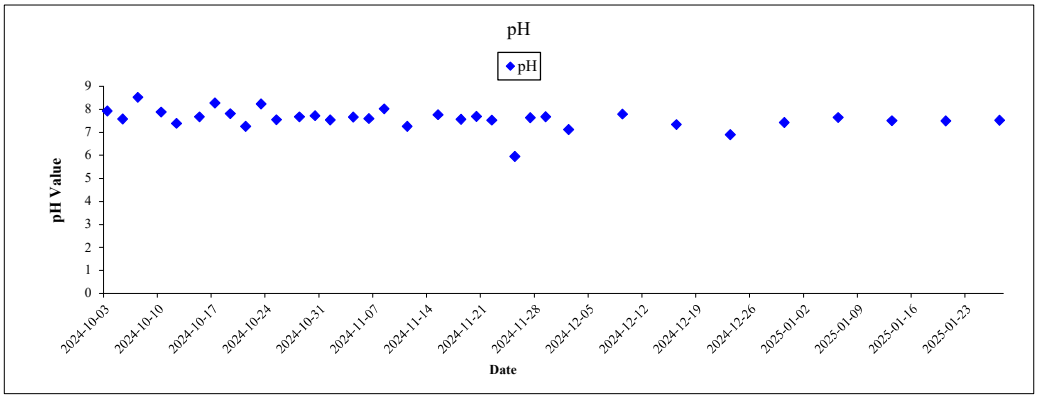


Monitoring Location: C2

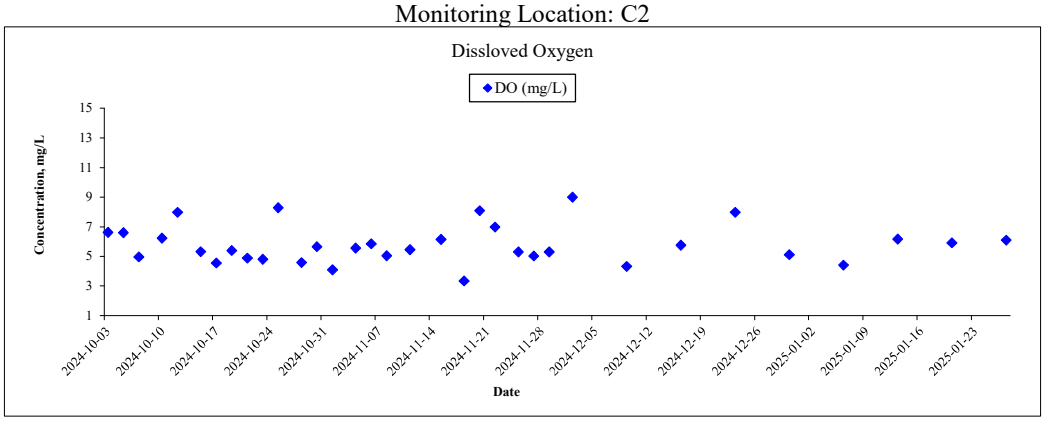


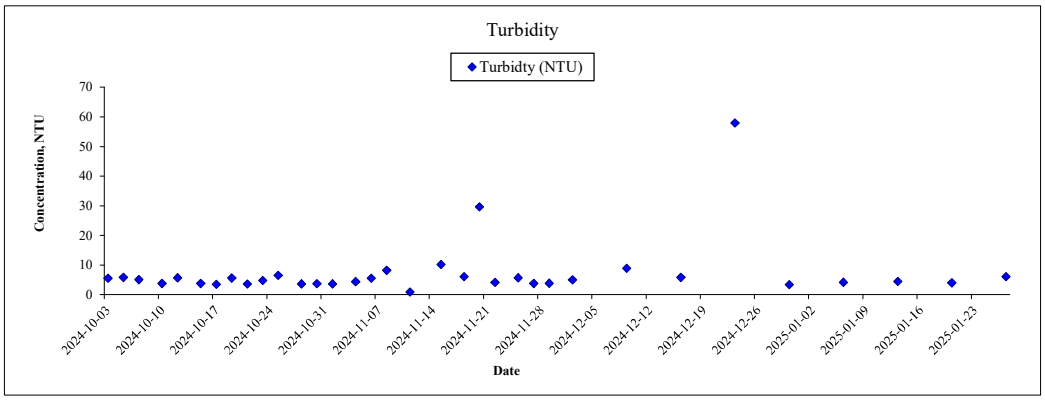


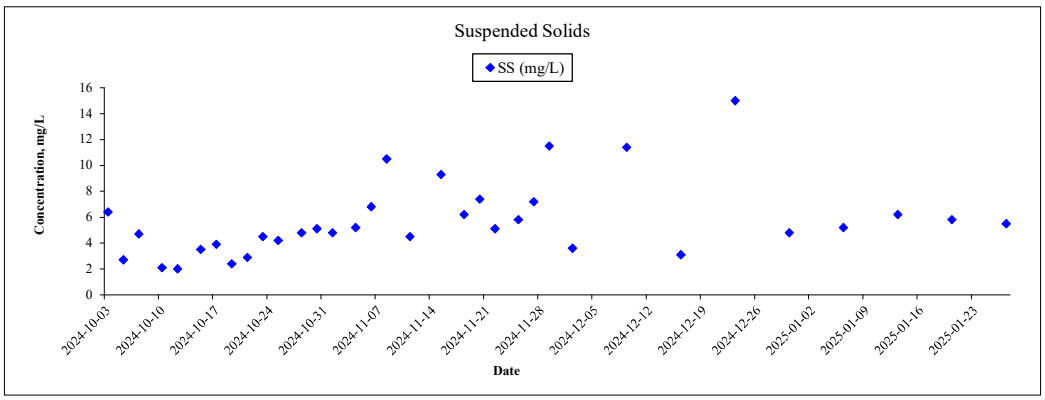


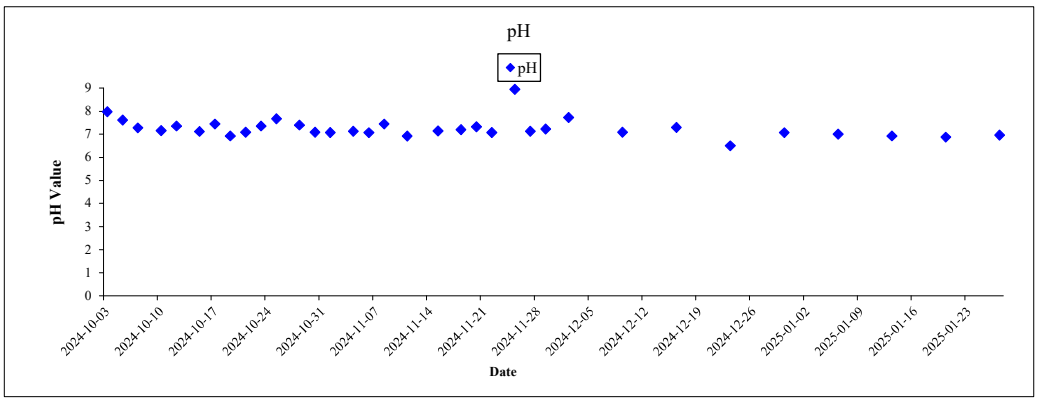


Monitoring Location: C1A

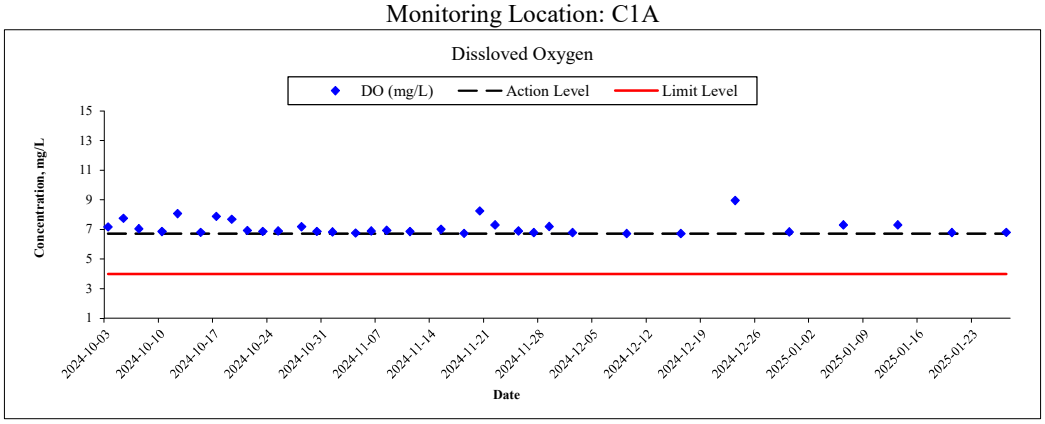

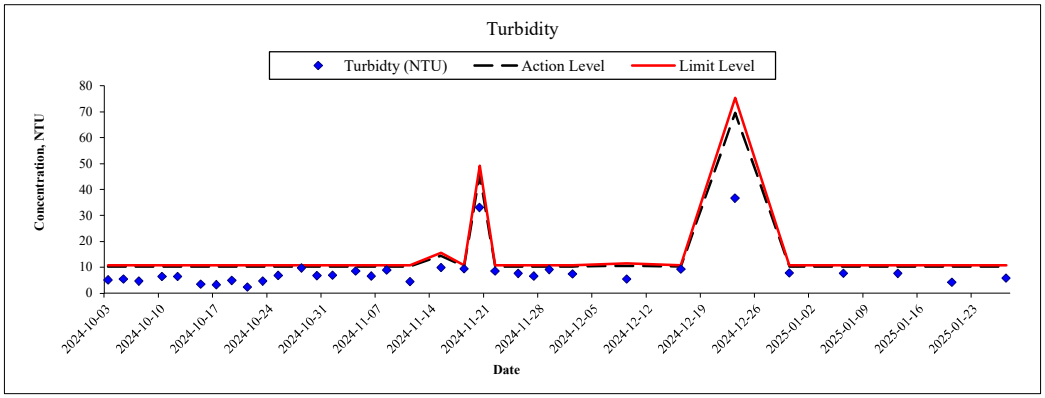

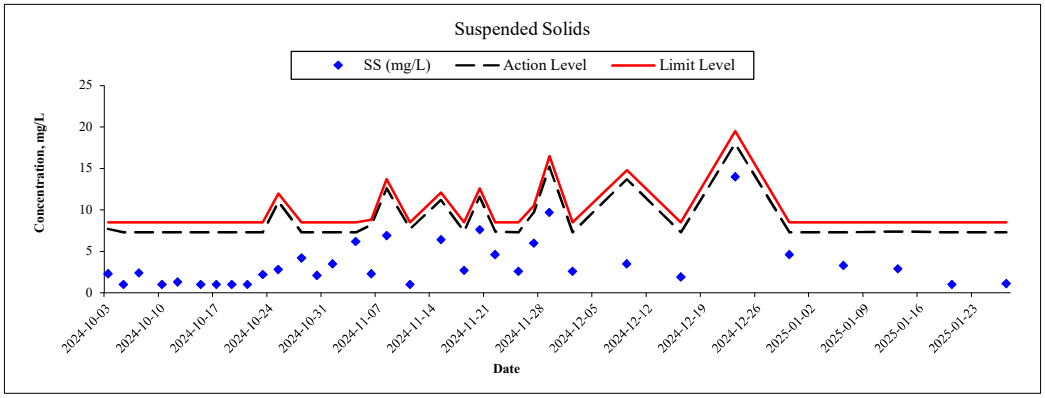

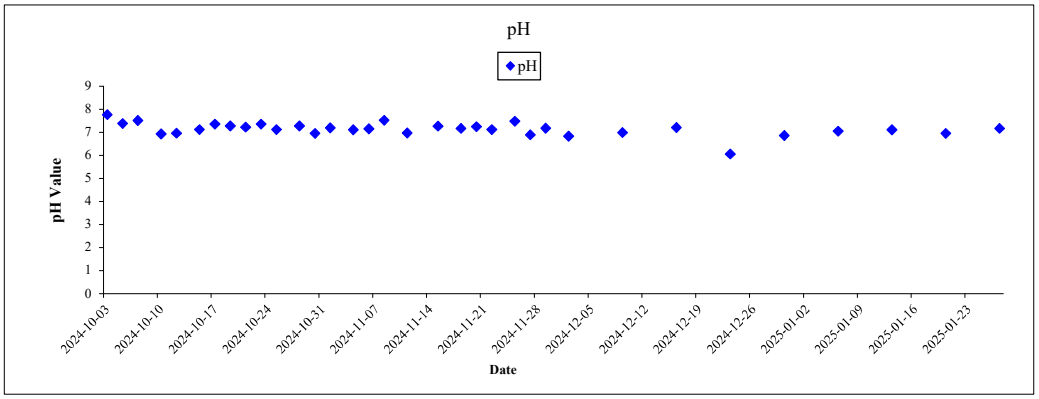



Appendix 3.1 Event and Action Plans for Noise


Event and Action Plan for Noise


Event	ET	IEC	ER	Contractor
Action Level	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and the Contractor and formulate remedial measures; and 5. Increase monitoring frequency to check the effectiveness of mitigation measures.	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; and 3. Advise the ER on the effectiveness of the proposed remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; and 4. Supervise the implementation of remedial measures.	1. Submit noise mitigation proposals to IEC and ER; and 2. Implement noise mitigation proposals.
Limit Level	1. Notify IEC, ER, EPD, and Contractor; 2. Identify source and investigate the cause of exceedance; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess the effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, and Contractor on the potential remedial actions; and 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; and 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; and 5. Stop the relevant portion of works as determined by ER, until the exceedance is abated.


Appendix 3.2 Graphical Presentation of Noise Monitoring

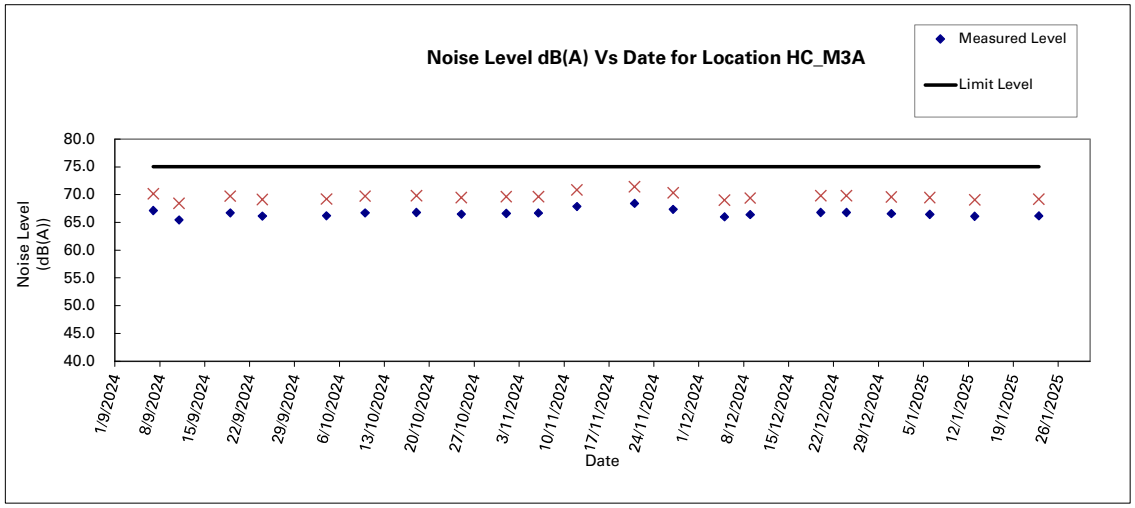

Noise Level dB(A) Vs Date for Location HC_M3A
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

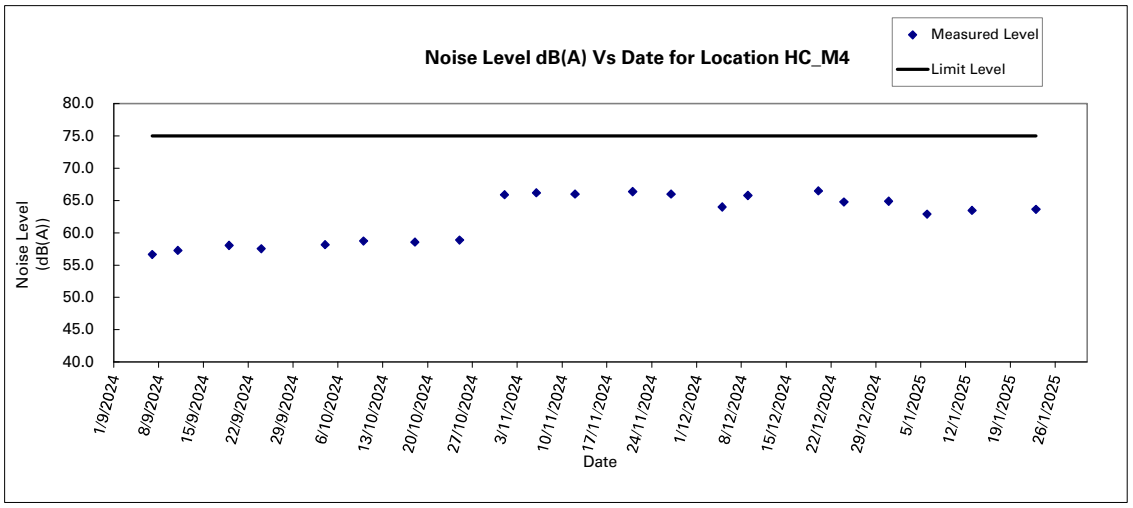

Noise Level dB(A) Vs Date for Location HC_M4
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

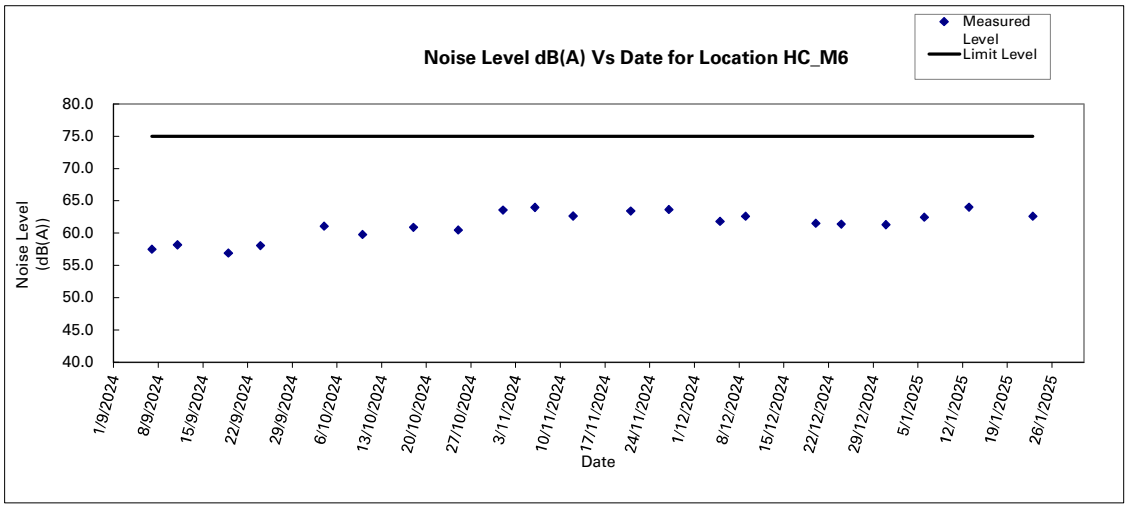

Noise Level dB(A) Vs Date for Location HC_M6
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

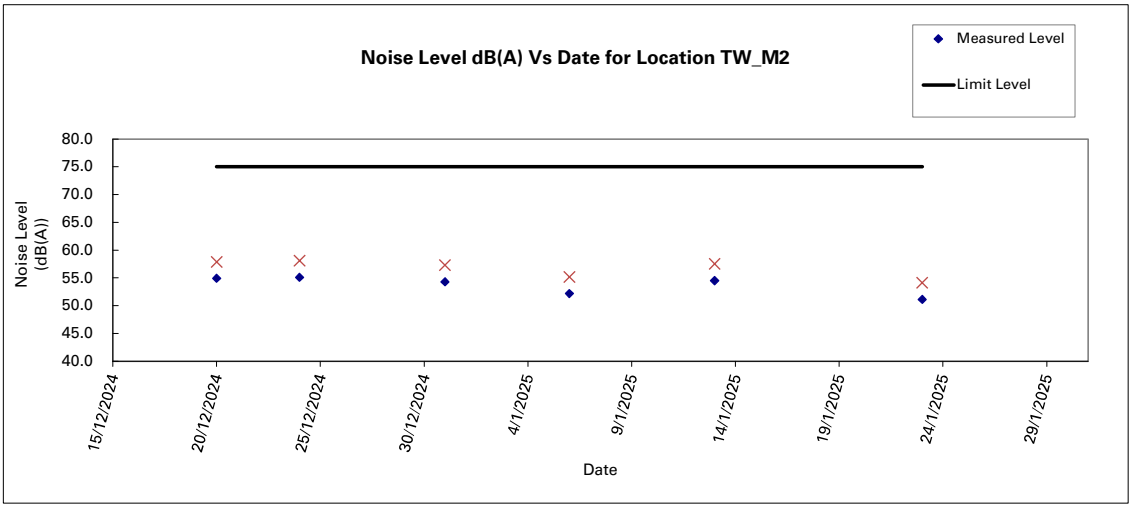

Noise Level dB(A) Vs Date for Location TW_M2
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
15/12/2024
20/12/2024
25/12/2024
30/12/2024
4/1/2025
9/1/2025
14/1/2025
19/1/2025
24/1/2025
29/1/2025
Date

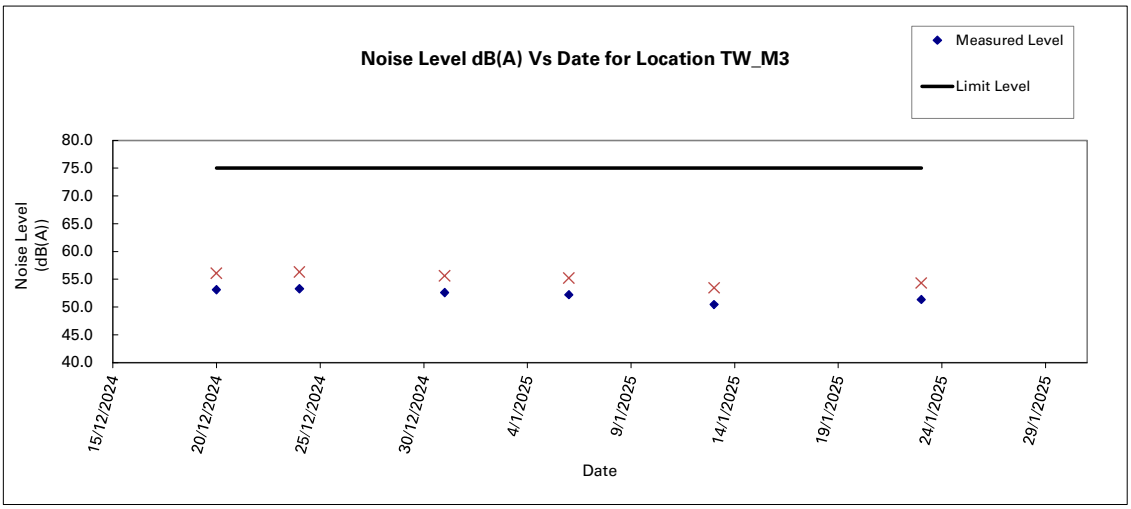

Noise Level dB(A) Vs Date for Location TW_M3
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
15/12/2024
20/12/2024
25/12/2024
30/12/2024
4/1/2025
9/1/2025
14/1/2025
19/1/2025
24/1/2025
29/1/2025
Date

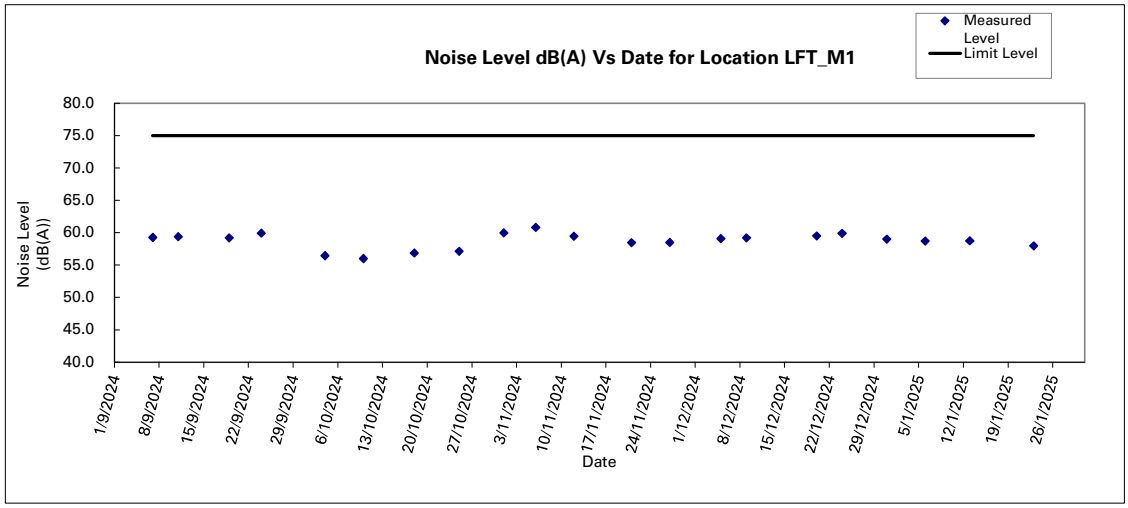

Noise Level dB(A) Vs Date for Location LFT_M1
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

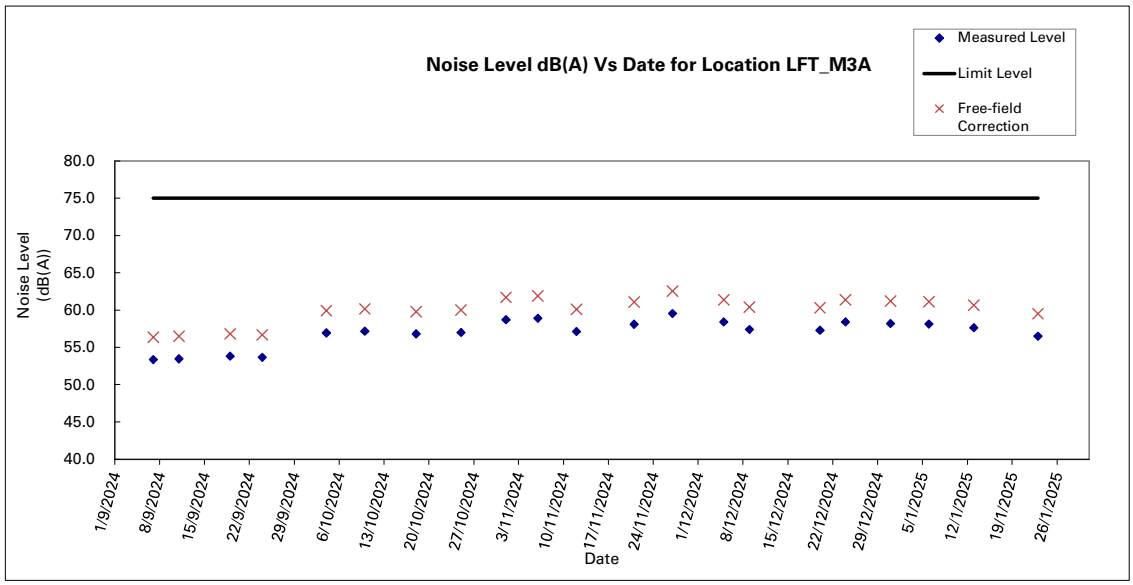

Noise Level dB(A) Vs Date for Location LFT_M3A
Measured Level
Limit Level
Free-field Correction
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

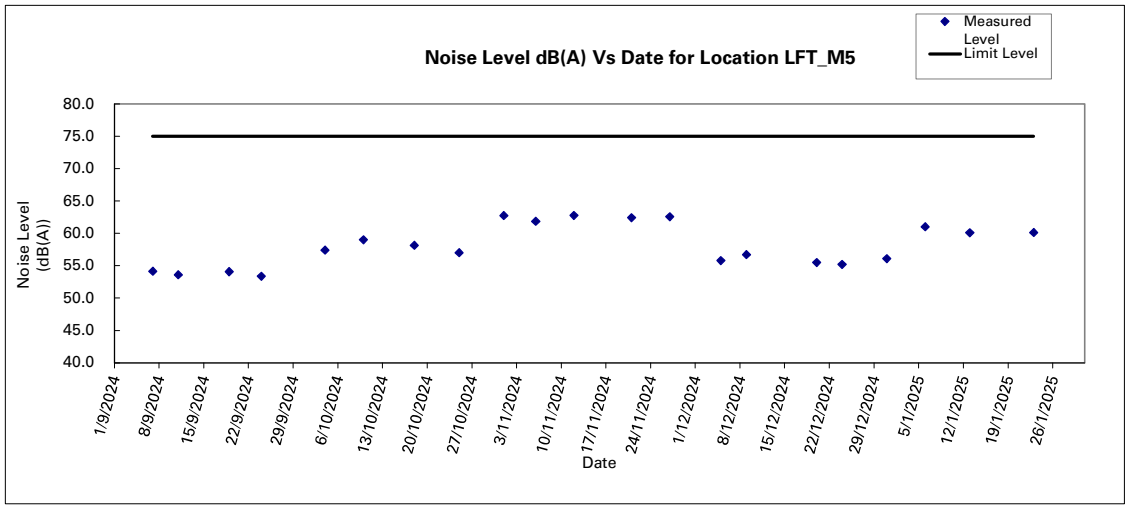

Noise Level dB(A) Vs Date for Location LFT_M5
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

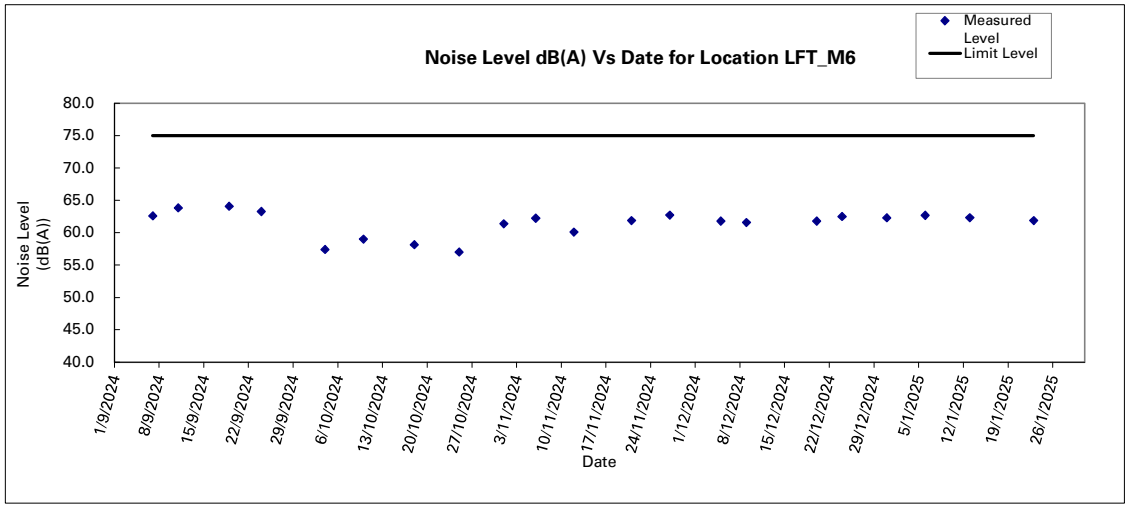
Noise Level dB(A) Vs Date for Location LFT_M6
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

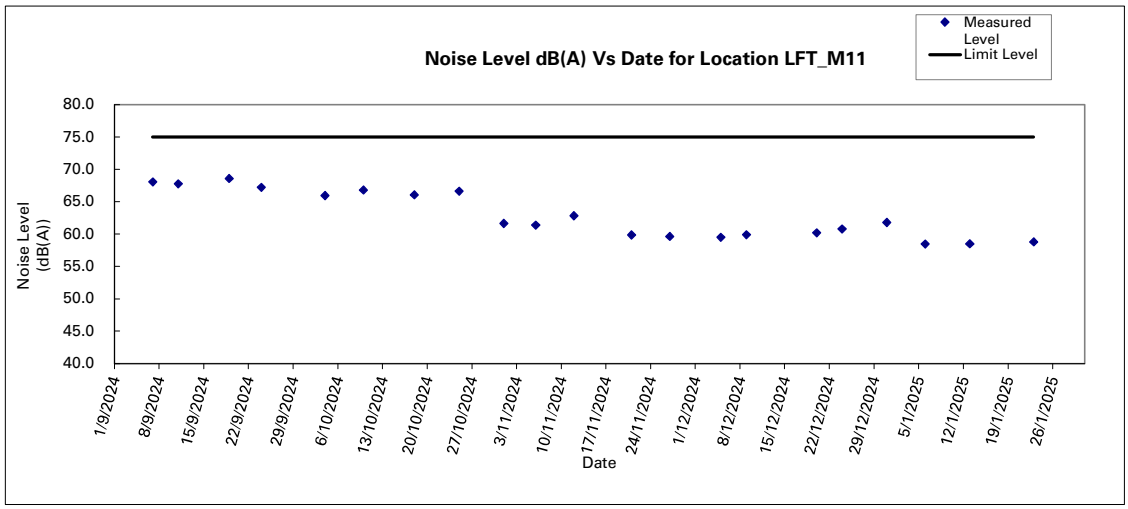
Noise Level dB(A) Vs Date for Location LFT_M11
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

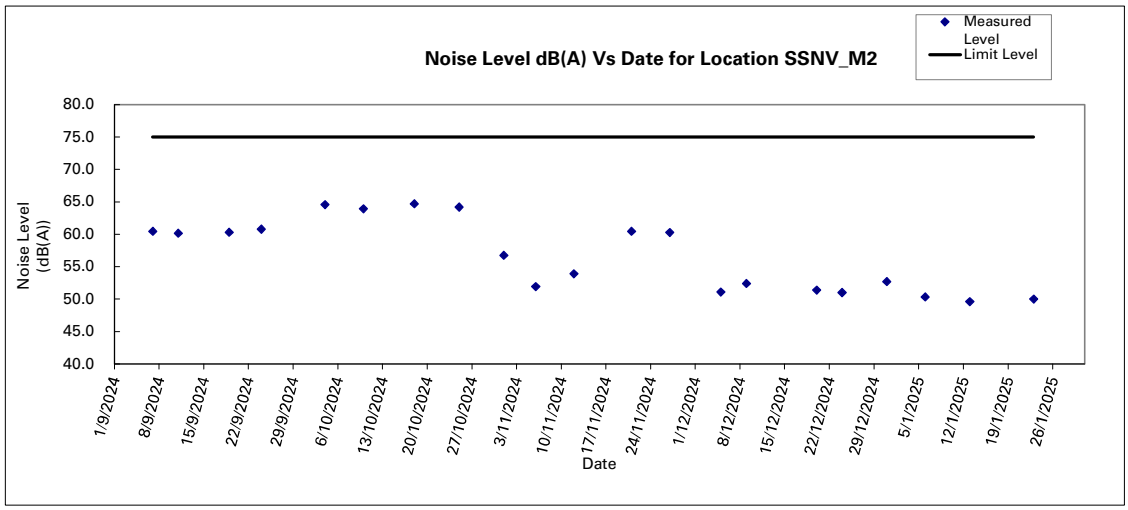
Noise Level dB(A) Vs Date for Location SSNV_M2
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

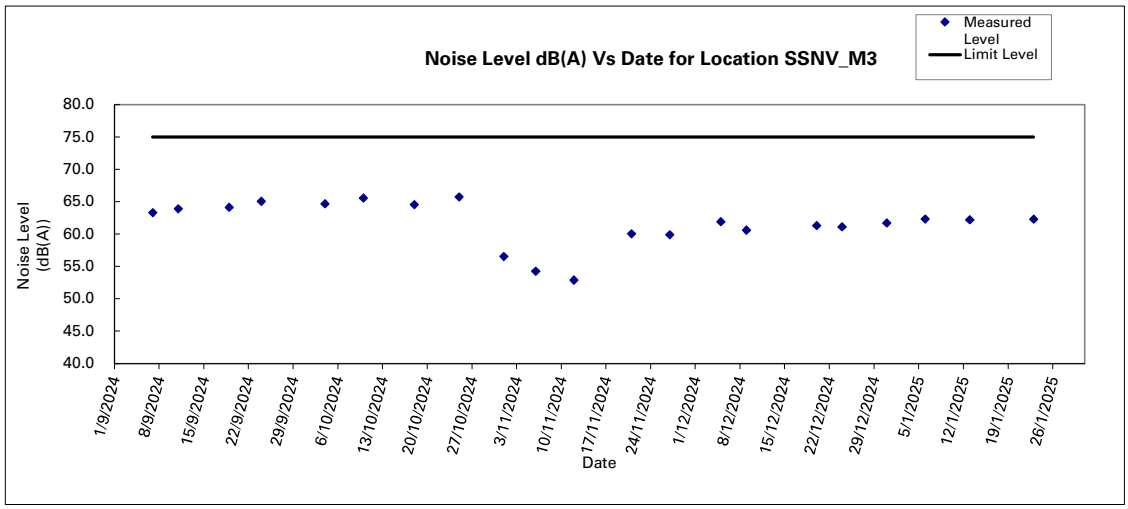
Noise Level dB(A) Vs Date for Location SSNV_M3
Measured Level
Limit Level
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

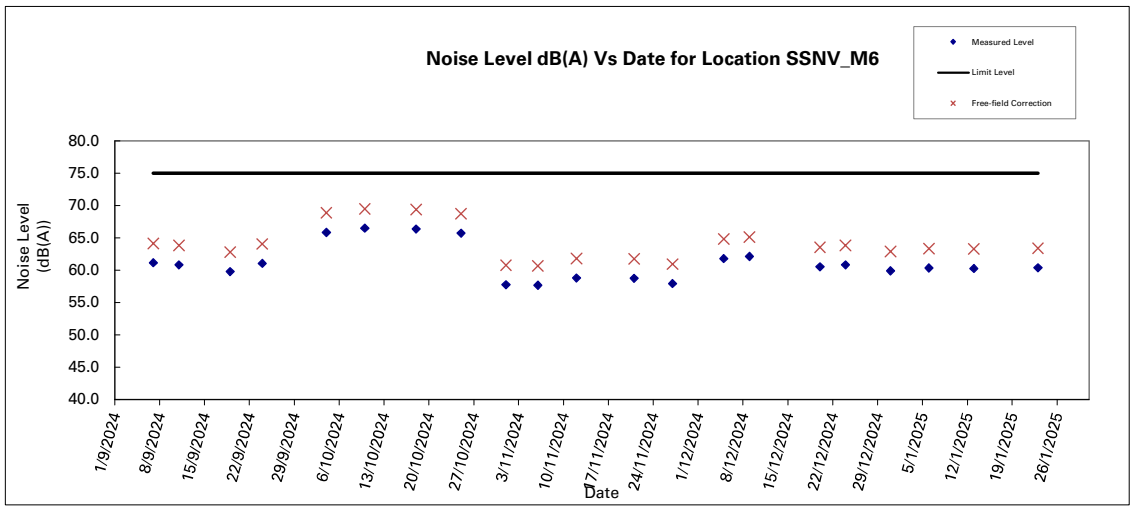
Noise Level dB(A) Vs Date for Location SSNV_M6
Measured Level
Limit Level
Free-field Correction
Noise Level (dB(A))
80.0
75.0
70.0
65.0
60.0
55.0
50.0
45.0
40.0
1/9/2024
8/9/2024
15/9/2024
22/9/2024
29/9/2024
6/10/2024
13/10/2024
20/10/2024
27/10/2024
3/11/2024
10/11/2024
17/11/2024
24/11/2024
1/12/2024
8/12/2024
15/12/2024
22/12/2024
29/12/2024
5/1/2025
12/1/2025
19/1/2025
26/1/2025
Date

Appendix 5.1 Waste Flow Table

Name of Department : Drainage Services Department

Contract No. : DC/2022/02

Monthly Summary Waste Flow Table for 2024

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastic	Chemical Waste	Others, e.g. General Refuse
	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m^3)
Jan	0.037	0.029	0.000	0.000	0.037	0.000	0.000	0.000	0.000	0.000	0.020
Feb	0.054	0.042	0.000	0.000	0.054	0.000	0.000	0.000	0.000	0.000	0.030
Mar	0.413	0.098	0.000	0.000	0.413	0.000	0.000	0.000	0.000	0.000	0.055
Apr	1.038	0.311	0.000	0.000	1.038	0.000	0.000	0.000	0.000	0.000	0.000
May	0.498	0.038	0.000	0.000	0.498	0.000	0.000	0.000	0.000	0.000	0.002
Jun	0.232	0.012	0.000	0.000	0.232	0.000	0.000	0.000	0.000	0.000	0.026
Sub-total	**2.273**	**0.531**	**0.000**	**0.000**	**2.273**	**0.000**	**0.000**	**0.000**	**0.000**	**0.000**	**0.133**
Jul	1.031	0.111	0.000	0.000	1.031	0.000	0.000	0.000	0.000	0.000	0.024
Aug	2.284	0.209	0.000	0.000	2.284	0.000	0.000	0.000	0.000	0.000	0.025
Sep	1.735	0.038	0.000	0.000	1.735	0.000	0.000	0.000	0.000	0.000	0.008
Oct	1.442	0.195	0.000	0.000	1.442	0.000	0.000	0.000	0.000	0.000	0.003
Nov	1.815	0.134	0.000	0.000	1.815	0.000	0.000	0.000	0.000	0.000	0.004
Dec	0.703	0.017	0.000	0.000	0.703	0.000	0.000	0.000	0.000	0.000	0.017
Total	**11.284**	**1.233**	**0.000**	**0.000**	**11.284**	**0.000**	**0.000**	**0.000**	**0.000**	**0.000**	**0.214**

Name of Department : Drainage Services Department

Contract No. : DC/2022/02

Monthly Summary Waste Flow Table for 2025

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastic	Chemical Waste	Others, e.g. General Refuse
	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m^3)
Jan	2.215	0.169	0.000	0.000	2.046	0.000	0.000	0.000	0.000	0.000	0.008
Feb											
Mar											
Apr											
May											
Jun											
Sub-total	**2.215**	**0.169**	**0.000**	**0.000**	**2.046**	**0.000**	**0.000**	**0.000**	**0.000**	**0.000**	**0.008**
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	**2.215**	**0.169**	**0.000**	**0.000**	**2.046**	**0.000**	**0.000**	**0.000**	**0.000**	**0.000**	**0.008**

Appendix 10.1 Complaint Log

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	**Cumulative**	**Complaint Nature**
1 Nov 2024 - 31 Jan 2025	2	3	One complaint regarding air quality and one complaint regarding water quality were recorded on 22 Jan 2025.

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	**Cumulative**	**Details**
1 Nov 2024 - 31 Jan 2025	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	**Cumulative**	**Details**
1 Nov 2024 - 31 Jan 2025	0	0	N/A

Document prepared by

Aurecon Hong Kong Limited

Unit 1608, 16/F, Tower B, Manulife Financial Centre,
223 – 231 Wai Yip Street, Kwun Tong, Kowloon
Hong Kong S. A. R.

T +852 3664 6888
F +852 3664 6999
E hongkong@aurecongroup.com
W aurecongroup.com

aurecon

Bringing ideas to life
