ID	Task Name	Duration	Start	Finish
1	Key Dates	1273 days	13-11-05	07-06-09
2	Commencement date	1 day	13-11-05	13-11-05
3	Section 1 completion key date	1 day	07-06-09	07-06-09
4	Section 2 completion key date	1 day	07-06-09	07-06-09
5	Stage I key date	1 day	10-01-06	10-01-06
6	Stage II key date	1 day	10-01-06	10-01-06
7	Stage III key date	1 day	14-06-06	14-06-06
8	Stage IV key date	1 day	14-06-06	14-06-06
9	Engineer's latest notice to cease	1 day	24-03-09	24-03-09
10	Preliminary	134 days	13-11-05	26-03-06
11	Design for combined reception/exit office	14 days	13-11-05	26-11-05
12	Engineer's approval	14 days	26-11-05	09-12-05
13	Design for CWBF	84 days	13-11-05	06-01-06
14	Design for Interim Manual Sorting	14 days	13-11-05	26-11-05
15	Engineer's approval	14 days	26-11-05	09-12-05
16	Design for Full-Scale Mechanical Sorting	28 days	26-11-05	23-12-05
17	Engineer's approval	14 days	24-12-05	06-01-06
18	Design for Lung Mun Road Run-in	14 days	13-11-05	26-11-05
19	Engineer & Hyd's approval	14 days	26-11-05	09-12-05
20	Procure mechanical sorting plant & equipment	78 days	07-01-06	26-03-06
21	Tseung Kwan O Area 137 (Section I)	1348 days	16-12-05	07-06-09
22	Combined Reception/ Exist Offices	25 days	16-12-05	03-01-06
23	Wheel washing facility & fences	14 days	16-12-05	23-12-05
24	Access Roads & Queuing Areas	25 days	16-12-05	03-01-06
25	Interim manual sorting facilities	25 days	16-12-05	03-01-06
26	Trial Operation Test & Approval	7 days	04-01-06	10-01-06
27	Stage I completion	0 days	10-01-06	10-01-06
28	Interim manual sorting	124 days	10-01-06	13-06-06
29	Install mechanical sorting plant & equipment	30 days	26-03-06	24-04-06
30	Testing mechanical sorting plant	13 days	25-04-06	07-05-06
31	Trial operation tests & approval	7 days	08-05-06	14-05-06
32	Stage III completion	0 days	14-06-06	14-06-06
33	Full scale mechanical sorting	1048 days	14-06-06	23-03-09
34	Cease operation	14 days	26-03-09	07-04-09
35	Demolish, remove & reinstate site	30 days	08-04-09	07-05-09
36	Section 1 completion	0 days	07-06-09	07-06-09
37	Yun Mun Area 38 (Section II)	1348 days	16-12-05	07-06-09
38	Combined reception/ Exist offices	25 days	16-12-05	03-01-06
39	Wheel washing facility & fencing	14 days	16-12-05	23-12-05
40	Access roads & Queuing areas	25 days	16-12-05	03-01-06
41	Lung Mun Road Transplanting	12 days	16-12-05	31-12-05
42	Lung Mun Road Run-in	13 days	23-12-05	03-01-06
43	Interim manual sorting facility	25 days	16-12-05	03-01-06
44	Trial operation test & approval	7 days	04-01-06	10-01-06
45	Stage II completion	0 days	10-01-06	10-01-06
46	Interim manual sorting	128 days	11-01-06	16-06-06
47	Install mechanical sorting plant & equipment	30 days	26-03-06	24-04-06
48	Testing mechanical sorting plant	13 days	25-04-06	07-05-06
49	Trial operation test & approval	7 days	08-05-06	14-05-06
50	Stage IV completion	0 days	14-06-06	14-06-06
51	Full scale mechanical sorting	1048 days	15-06-06	24-03-09
52	Cease operations	14 days	26-03-09	07-04-09
53	Demolish, remove & reinstate	30 days	08-04-09	07-05-09
54	Section 2 completion	0 days	07-06-09	07-06-09

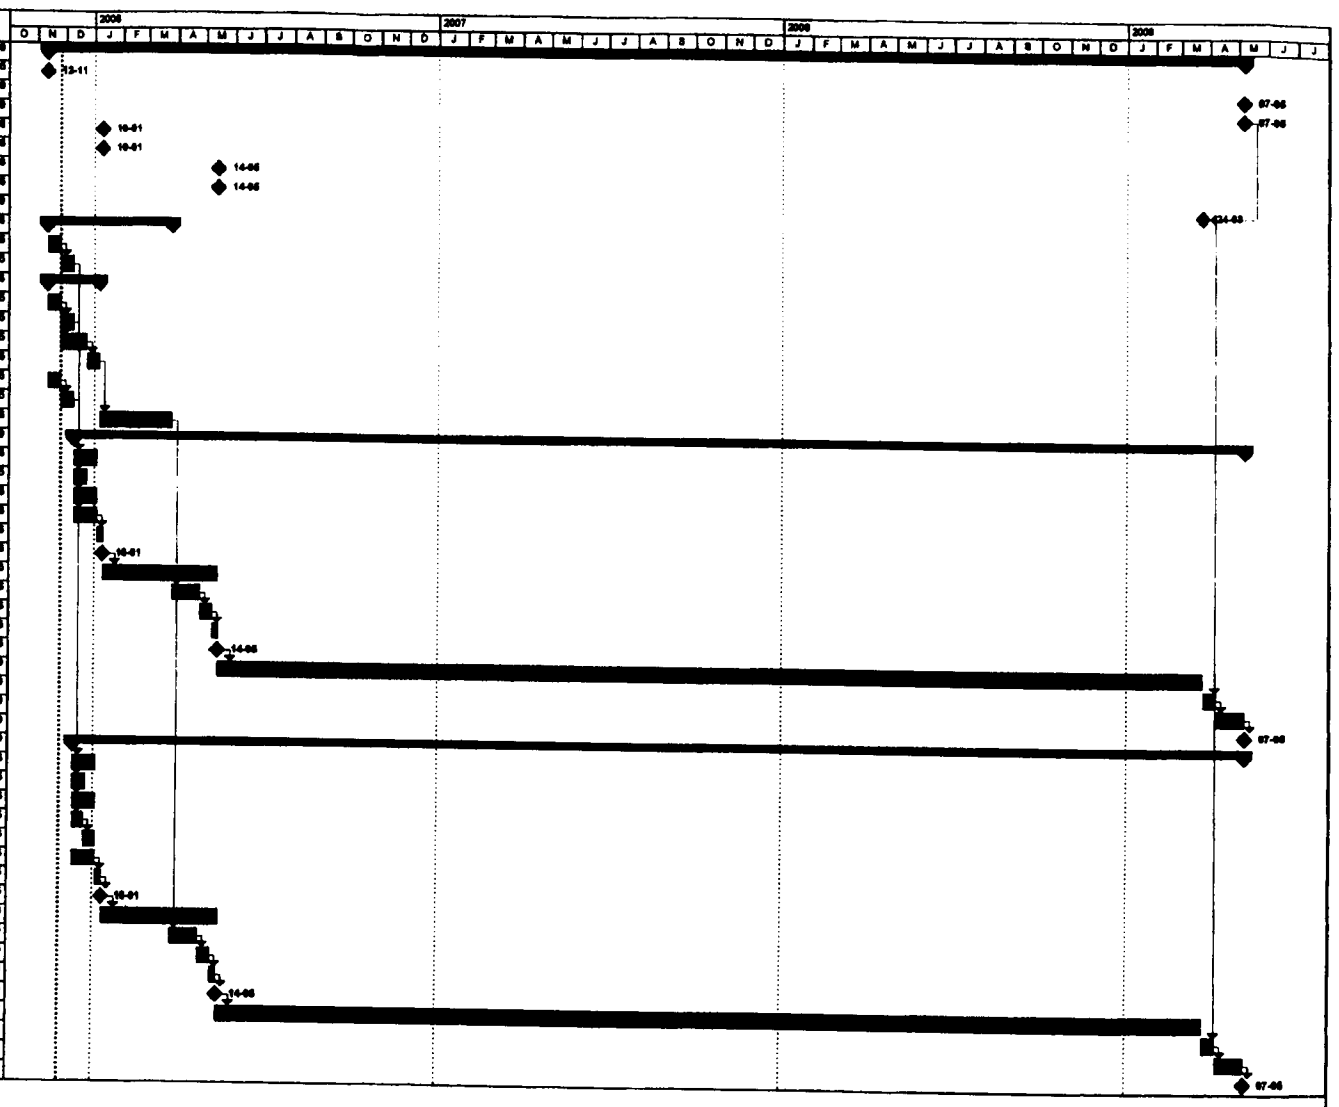

Programme no. : WP02
Date: 25-11-05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | External Milestone | External Milestone | External Milestone | Deadline

CEDD Contract no.: CV/2004/13
Temporary Construction Waste Sorting Facilities
at Tseung Kwan O Area 37 and Tuen Mun Area 38

Works Programme (Rev. A)

Paul Y. - CHEC Joint Venture
