Maeda Corporation
Contract No. DC/2005/01
Expansion of Shek Wu Hui Sewage Treatment Works and
Upgrading of Ting Kok Road Pumping Station No.5
Master Programme (Rev. 6)

ID		Task Name	Duration	Start	Finish	Preds
649	✓	Preliminary Pile	30 days	Thu 05/12/22	Wed 06/1/25	648
650	✓	Installation of Re-bars	32 days	Sat 06/3/11	Tue 06/4/18	649
651	✓	Grouting	32 days	Mon 06/3/13	Tue 06/4/18	649
652	✓	Post Drilling	10 days	Tue 06/4/11	Fri 06/4/21	
653	✓	Loading Test	5 days	Tue 06/4/25	Sat 06/4/29	
654	✓	Site Clearance	3 days	Thu 06/4/20	Sat 06/4/22	651
655		Transformer House	232 days	Tue 06/5/16	Fri 07/2/9	
656		Diversion of Existing Sewer	50 days	Tue 06/5/16	Wed 06/7/12	
657		Construction of Substructure	61 days	Thu 06/7/13	Thu 06/9/21	
658		Temporary Works (Sheet Pile + Open Cut)	16 days	Thu 06/7/13	Mon 06/7/31	656
659		Lift 1 (from +3.95 mPD to +4.95 mPD)	15 days	Tue 06/8/1	Thu 06/8/17	658
660		Lift 2 (from +4.95 mPD to +5.95 mPD)	15 days	Fri 06/8/18	Mon 06/9/4	659
661		Lift 3 (from +5.15 mPD to +6.15 mPD)	15 days	Tue 06/9/5	Thu 06/9/21	660
662		Construction of Superstructure	40 days	Fri 06/9/22	Tue 06/11/7	
663		Lift 4 (from +6.15 mPD to +11.20 mPD)	20 days	Fri 06/9/22	Sat 06/10/14	661
664		Lift 5 (from +11.20 mPD to +12.30 mPD)	20 days	Mon 06/10/16	Tue 06/11/7	663
665		Internal Finishes (incl. Plumbing, cat ladder, etc.)	22 days	Tue 07/1/16	Fri 07/2/9	
666		Ting Kok Road Pumping Station No.5	312 days	Wed 06/5/3	Tue 07/5/1	
667	✓	General Excavation & Trial Trench	5 days	Wed 06/5/3	Mon 06/5/8	
668		Sheet Piling	50 days	Tue 06/6/27	Wed 06/8/23	667
669		ELS Works for Pumping Station No. 5	60 days	Fri 06/8/25	Thu 06/11/2	668
670		Sub-structure works for Pumping Station No. 5	113 days	Tue 06/10/24	Sat 07/3/3	
671		Lift 1 (from -4.08 mPD to -2.35 mPD)	20 days	Tue 06/10/24	Wed 06/11/15	
672		Lift 2 (from -2.35mPD to -1.25 mPD)	20 days	Thu 06/11/16	Fri 06/12/8	671
673		Lift 3 (from -1.25 mPD to +2.5mPD)	18 days	Sat 06/12/9	Fri 06/12/29	672
674		Lift 4 (from +2.50mPD to +5.30mPD)	34 days	Sat 06/12/30	Wed 07/2/7	673
675		Lift 5 (from +2.50mPD to +6.30mPD)	21 days	Thu 07/2/8	Sat 07/3/3	674
676		Water Tightness Test	19 days	Mon 07/3/5	Mon 07/3/26	675
677		**Superstructure works for Pumping Station No. 5**	**29 days**	**Mon 07/3/5**	**Fri 07/4/6**	
678		Lift 6 (from +6.30mPD to +13.20mPD)	15 days	Mon 07/3/5	Wed 07/3/21	675
679		Lift 7 (from +13.20mPD to +14.30mPD)	14 days	Thu 07/3/22	Fri 07/4/6	678
680		Internal Finishes (incl. Plumbing, cat ladder, etc.)	21 days	Sat 07/4/7	Tue 07/5/1	679
681		Key date of Section 6 of the Works	1 day	Tue 07/5/1	Tue 07/5/1	
682		Section 7 of the Works	443 days	Fri 06/3/31	Wed 07/8/29	
683		Pipe Jacking	179 days	Wed 06/4/19	Mon 06/11/13	
684		TL2	50 days	Wed 06/4/19	Thu 06/6/15	
685		TL3	133 days	Mon 06/5/15	Mon 06/10/16	
686		TL1	81 days	Fri 06/8/11	Mon 06/11/13	
687		Twin 450mm Rising Mains	220 days	Thu 06/7/20	Mon 07/4/2	
688		Portion 1 (12m)	39 days	Thu 06/7/20	Sat 06/9/2	
689		Portion 2 (24m)	12 days	Mon 06/9/4	Sat 06/9/16	688
690		Portion 3 (24m)	12 days	Mon 06/9/18	Sat 06/9/30	689
691		Portion 4 (24m)	12 days	Mon 06/10/2	Sat 06/10/14	690
692		Portion 5 (24m)	12 days	Mon 06/10/16	Sat 06/10/28	691
693		Portion 6 (24m)	12 days	Mon 06/10/30	Sat 06/11/11	692
694		Portion 7 (24m)	12 days	Mon 06/11/13	Sat 06/11/25	693
695		Portion 8 (24m)	12 days	Mon 06/11/27	Sat 06/12/9	694
696		Portion 9 (24m)	12 days	Mon 06/12/11	Sat 06/12/23	695
697		Portion 10 (24m)	12 days	Mon 06/12/25	Sat 07/1/6	696
698		Portion 11 (24m)	12 days	Mon 07/1/8	Sat 07/1/20	697
699		Portion 12 (24m)	12 days	Mon 07/1/22	Sat 07/2/3	698
700		Portion 13 (24m)	12 days	Mon 07/2/5	Sat 07/2/17	699
701		Portion 14 (24m)	12 days	Mon 07/2/19	Sat 07/3/3	700
702		Portion 15 (24m)	12 days	Mon 07/3/5	Sat 07/3/17	701

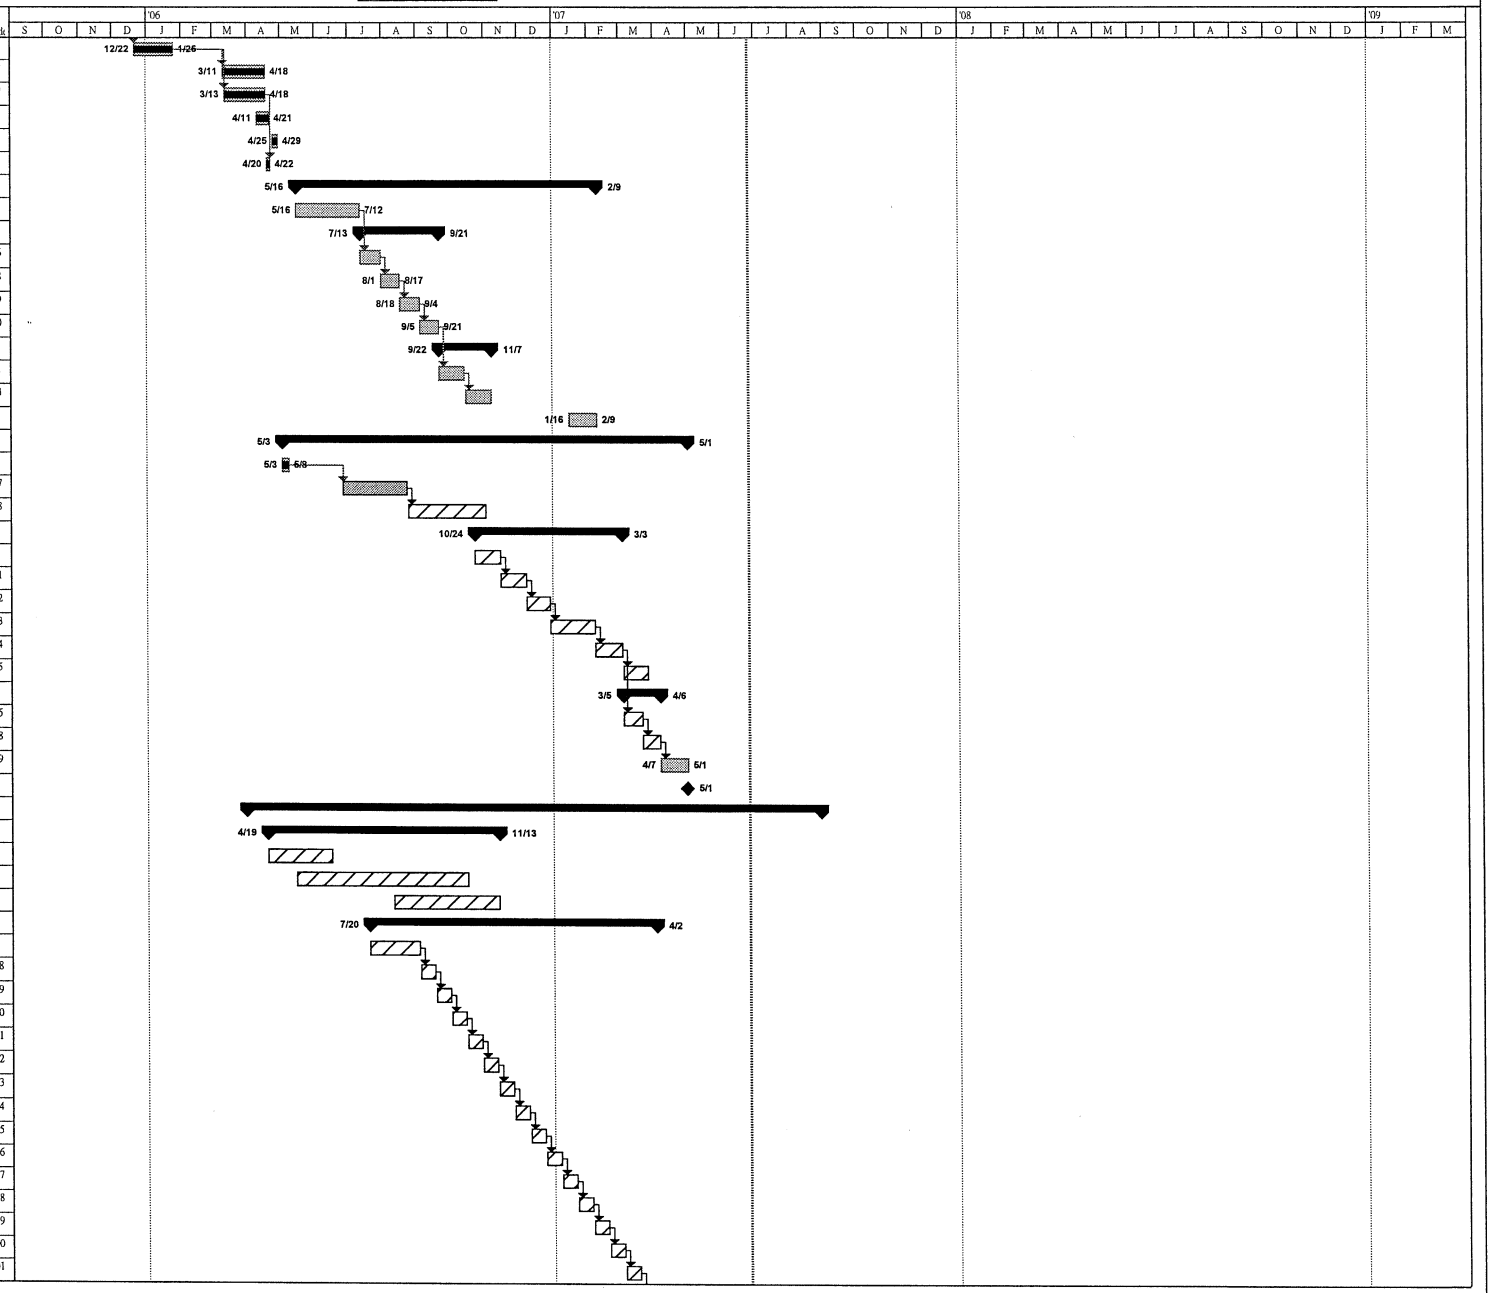

Date: Mon 07/6/25

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary

Maeda Corporation
Contract No. DC/2005/01
Expansion of Shek Wu Hui Sewage Treatment Works and
Upgrading of Ting Kok Road Pumping Station No.5
Master Programme (Rev. 6)

ID		Task Name	Duration	Start	Finish	Predk
703		Portion 16 (12m)	12 days	Mon 07/3/19	Sat 07/3/31	702
704		Testing of pipeline	1 day	Mon 07/4/2	Mon 07/4/2	703
705		Gravity Sewers and Manholes	351 days	Fri 06/3/31	Mon 07/5/14	
706		Excavation of Trial Pits	40 days	Fri 06/3/31	Tue 06/5/16	
707		Stage 2 (MH8 - MH9)	107 days	Wed 06/9/13	Mon 07/1/15	706
708		Stage 1 and 1A(V.O. MH8 - MH7A - MH7)	30 days	Tue 07/1/16	Mon 07/2/19	707
709		Stage 3 (MH9 - MH10)	30 days	Tue 07/2/20	Mon 07/3/26	708
710		Stage 4 (MH10 - Existing Manhole)	37 days	Tue 07/3/27	Tue 07/5/8	709
711		CCTV Inspection	5 days	Wed 07/5/9	Mon 07/5/14	710
712		Ting Kok Road Pumping Station No. 5 (Pipeworks)	128 days	Tue 07/4/3	Wed 07/8/29	
713		Laying Sewer MH6 - MH5 (by trenchless method)	4 days	Tue 07/4/3	Fri 07/4/6	704
714		Construction of MH6	3 days	Sat 07/4/7	Tue 07/4/10	713
715		Construction of MH5	3 days	Wed 07/4/11	Fri 07/4/13	714
716		Sheet Piling and Excavation (Type E & F)	30 days	Tue 07/4/3	Mon 07/5/7	704
717		Laying Sewer MH5 - MH4	8 days	Sat 07/4/14	Mon 07/4/23	715
718		Construction of MH4	8 days	Tue 07/4/24	Wed 07/5/2	717
719		Laying Sewer MH4 - MH3	8 days	Thu 07/5/3	Fri 07/5/11	718
720		Construction of MH3	8 days	Sat 07/5/12	Mon 07/5/21	719
721		Laying Sewer MH3 - MH2	8 days	Tue 07/5/22	Wed 07/5/30	720
722		Construction of MH2	8 days	Thu 07/5/31	Fri 07/6/8	721
723		Laying Sewer MH2 - MH1	8 days	Sat 07/6/9	Mon 07/6/18	722
724		Construction of MH1	8 days	Tue 07/6/19	Wed 07/6/27	723
725		Laying Sewer MH4 - F2	8 days	Thu 07/6/28	Fri 07/7/6	724
726		Modification of F2	8 days	Sat 07/7/7	Mon 07/7/16	725
727		Laying Sewer P/S - MH6	8 days	Tue 07/7/17	Wed 07/7/25	726
728		Testing of pipeline	8 days	Thu 07/7/26	Fri 07/8/3	727
729		Laying Sewer P/S - Existing box culvert	8 days	Sat 07/8/4	Mon 07/8/13	728
730		Connection to existing box culvert	8 days	Tue 07/8/14	Wed 07/8/22	729
731		CCTVInspection	6 days	Thu 07/8/23	Wed 07/8/29	730
732		Remaining Works for P/S and T/H	142 days	Thu 07/3/1	Mon 07/8/13	
733		Civil works for E&M installation (Cable Ducts & Draw Pits)	135 days	Fri 07/3/9	Mon 07/8/13	
734		External Finishes	120 days	Thu 07/3/1	Wed 07/7/18	
735		Roofing Finishes	43 days	Thu 07/3/1	Thu 07/4/19	
736		Key Date of Section 7 of the Works	1 day	Wed 07/8/29	Wed 07/8/29	
737		Section 8 - All Remaining Works	183 days	Thu 07/4/26	Sat 07/11/24	
738		E&M installation (by Others)	157 days	Thu 07/4/26	Thu 07/10/25	
739		External Cable Duct, Drainage & Catchpit	55 days	Tue 07/8/14	Tue 07/10/16	733
740		Construction of Boundary Wall	58 days	Tue 07/8/14	Fri 07/10/19	733
741		Demolition of Existing Boundary Wall	7 days	Sat 07/10/20	Sat 07/10/27	740
742		Road Paving	21 days	Sat 07/10/20	Tue 07/11/13	739,.
743		Testing and Commissioning (by Others)	80 days	Wed 07/8/15	Thu 07/11/15	
744		Connection to MH F2	7 days	Mon 07/7/23	Mon 07/7/30	
745		Connection to MH1	7 days	Mon 07/7/23	Mon 07/7/30	
746		Demolition of existing pumping pit	7 days	Tue 07/7/31	Tue 07/8/7	744,.
747		Grouting for Existing Sewer & Manhole	30 days	Wed 07/8/8	Tue 07/9/11	746
748		Landscaping	30 days	Wed 07/9/12	Tue 07/10/16	747
749		Establishment works	34 days	Wed 07/10/17	Sat 07/11/24	748
750		Key Date of Section 8 of the Works	1 day	Sat 07/11/24	Sat 07/11/24	

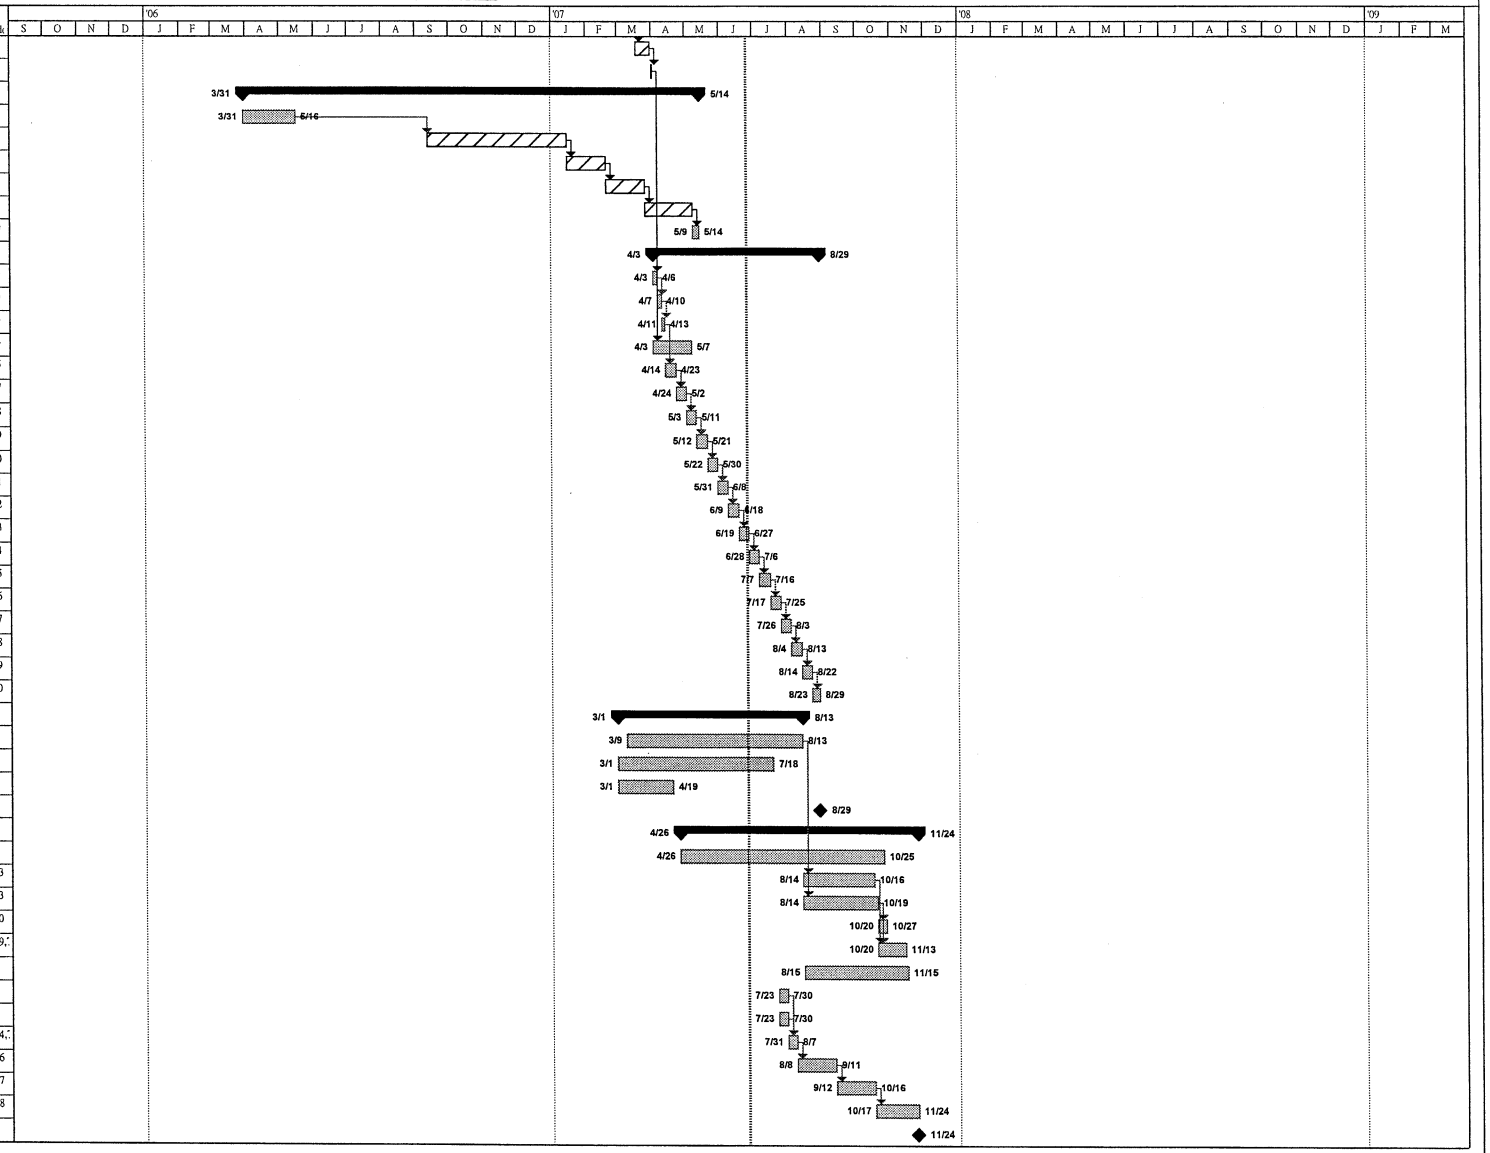

Date: Mon 07/6/25

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary
