Macda Corporation
Contract No. DC/2005/01
Expansion of Shek Wu Hui Sewage Treatment Works and
Upgrading of Ting Kok Road Pumping Station No.5
Master Programme (Rev. 6A)

ID		Task Name	Duration	Start	Finish
305		**Superstructure works for Pumping Station No. 5**	**29 days**	**Sat 07/3/3**	**Thu 07/4/5**
306		Lift 6 (from +6.30mPD to +13.20mPD)	15 days	Sat 07/3/3	Tue 07/3/20
307		Lift 7 (from +13.20mPD to +14.30mPD)	14 days	Wed 07/3/21	Thu 07/4/5
308		Internal Finishes (incl. Plumbing, cat ladder, etc.)	21 days	Fri 07/4/6	Mon 07/4/30
309		Key date of Section 6 of the Works	1 day	Tue 07/5/1	Tue 07/5/1
310		Section 7 of the Works	487 days	Fri 06/3/31	Thu 07/10/18
311		Pipe Jacking	179 days	Wed 06/4/19	Mon 06/11/13
312		TL2	50 days	Wed 06/4/19	Thu 06/6/15
313		TL3	133 days	Mon 06/5/15	Mon 06/10/16
314		TL1	81 days	Fri 06/8/11	Mon 06/11/13
315		Twin 450mm Rising Mains	315 days	Thu 06/7/20	Fri 07/7/20
316		Portion 1 (12m)	39 days	Thu 06/7/20	Sat 06/9/2
317		Portion 2 (24m)	18 days	Mon 06/9/4	Sat 06/9/23
318		Portion 3 (24m)	18 days	Mon 06/9/25	Sat 06/10/14
319		Portion 4 (24m)	18 days	Mon 06/10/16	Sat 06/11/4
320		Portion 5 (24m)	18 days	Mon 06/11/6	Sat 06/11/25
321		Portion 6 (24m)	18 days	Mon 06/11/27	Fri 06/12/15
322		Portion 7 (24m)	18 days	Sat 06/12/16	Fri 07/1/5
323		Portion 8 (24m)	18 days	Sat 07/1/6	Fri 07/1/26
324		Portion 9 (24m)	18 days	Sat 07/1/27	Fri 07/2/16
325		Portion 10 (24m)	18 days	Sat 07/2/17	Fri 07/3/9
326		Portion 11 (24m)	18 days	Sat 07/3/10	Fri 07/3/30
327		Portion 12 (24m)	18 days	Sat 07/3/31	Fri 07/4/20
328		Portion 13 (24m)	18 days	Sat 07/4/21	Fri 07/5/11
329		Portion 14 (24m)	18 days	Sat 07/5/12	Fri 07/6/1
330		Portion 15 (24m)	18 days	Sat 07/6/2	Fri 07/6/22
331		Portion 16 (12m)	18 days	Sat 07/6/23	Fri 07/7/13
332		Pressure Test & CCTV	6 days	Sat 07/7/14	Fri 07/7/20
333		Gravity Sewers and Manholes	444 days	Fri 06/3/31	Wed 07/8/29
334		Excavation of Trial Pits	40 days	Fri 06/3/31	Tue 06/5/16
335		Stage 2 (MH8 - MH9)	107 days	Thu 06/9/14	Mon 07/1/15
336		Stage 1 and 1A(V.O. MH8 - MH7A - MH7)	139 days	Tue 07/1/16	Tue 07/6/26
337		Stage 3 (MH9 - MH10)	25 days	Wed 07/6/27	Wed 07/7/25
338		Stage 4 (MH10 - Existing Manhole)	25 days	Thu 07/7/26	Thu 07/8/23
339		CCTV Inspection	5 days	Fri 07/8/24	Wed 07/8/29
340		Ting Kok Road Pumping Station No. 5 (Pipeworks)	330 days	Fri 06/8/11	Wed 07/8/29
341		Laying Sewer MH6 - MH5 (by trenchless method)	81 days	Fri 06/8/11	Mon 06/11/13
342		Construction of MH6	23 days	Sat 07/1/6	Thu 07/2/1

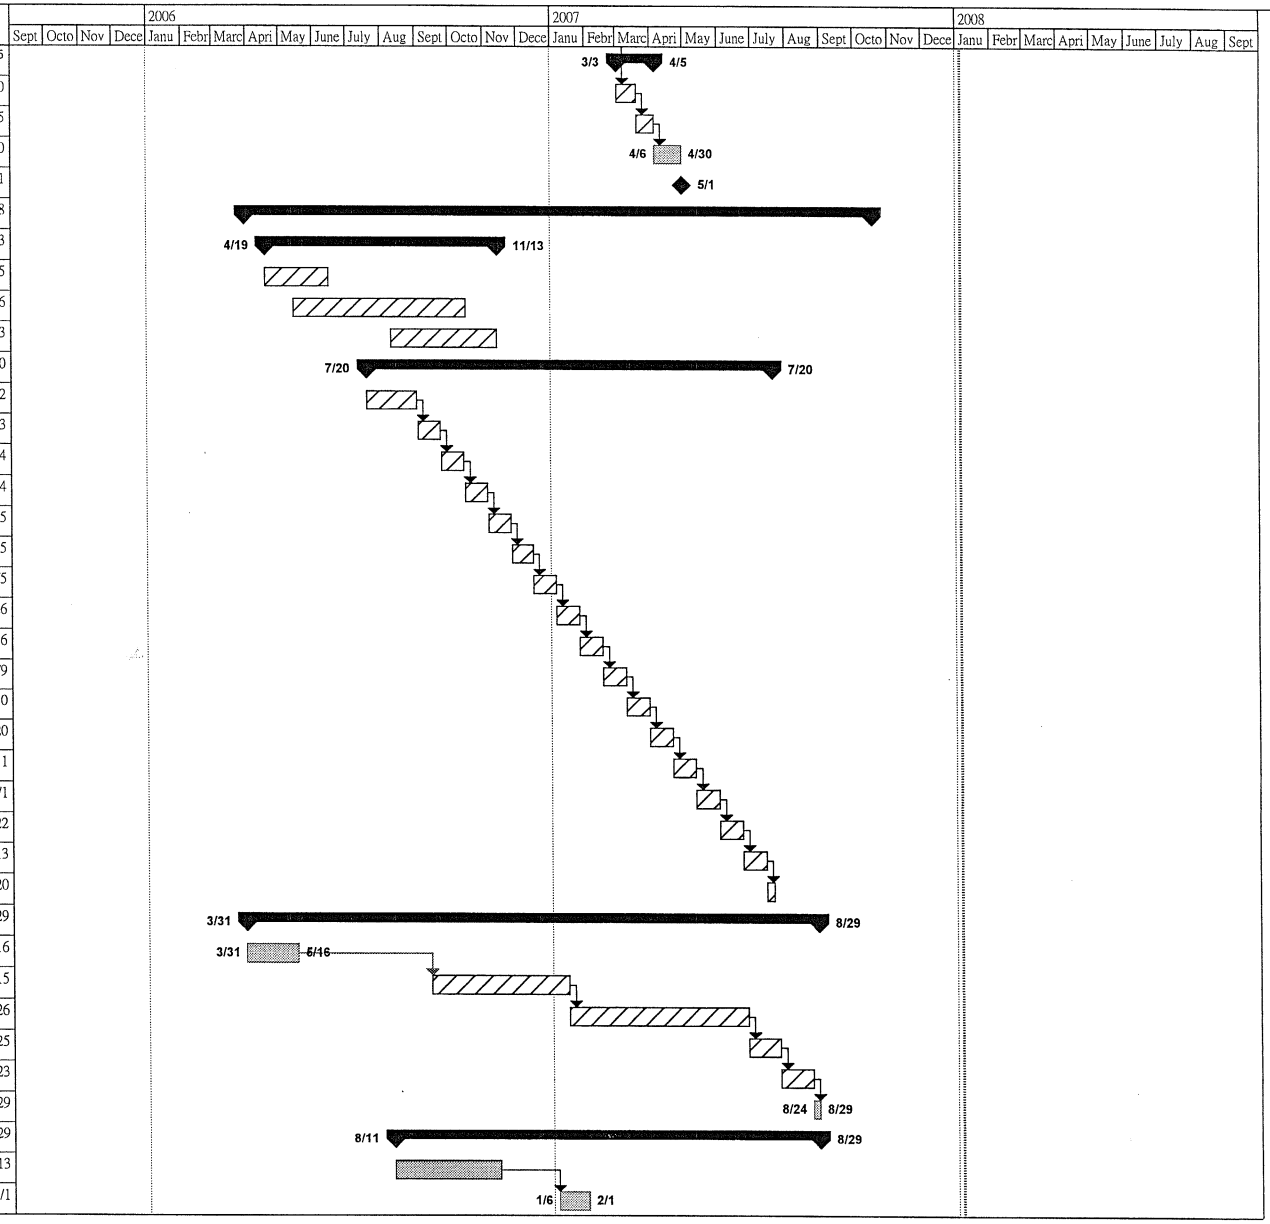

Date: Sat 08/1/5

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary

Maeda Corporation
Contract No. DC/2005/01
Expansion of Shek Wu Hui Sewage Treatment Works and
Upgrading of Ting Kok Road Pumping Station No.5
Master Programme (Rev. 6A)

ID		Task Name	Duration	Start	Finish
343		Construction of MH5	24 days	Fri 07/1/12	Thu 07/2/8
344		Sheet Piling and Excavation (Type E & F)	29 days	Thu 07/4/12	Tue 07/5/15
345		Laying Sewer MH5 - MH4	47 days	Wed 07/5/16	Mon 07/7/9
346		Construction of MH4	8 days	Tue 07/7/10	Wed 07/7/18
347		Laying Sewer MH4 - MH3	8 days	Thu 07/7/19	Fri 07/7/27
348		Construction of MH3	8 days	Sat 07/7/28	Mon 07/8/6
349		Construction of MH 13	8 days	Tue 07/8/7	Wed 07/8/15
350		Connection of MH 3 to Existing Sewer	8 days	Thu 07/8/16	Fri 07/8/24
351		Testing of pipeline	2 days	Sat 07/8/25	Mon 07/8/27
352		CCTVInspection	2 days	Tue 07/8/28	Wed 07/8/29
353		Remaining Works for P/S and T/H	199 days	Thu 07/3/1	Thu 07/10/18
354		Civil works for E&M installation (Cable Ducts & Draw Pits)	47 days	Sat 07/8/25	Thu 07/10/18
355		External Finishes	120 days	Thu 07/3/1	Wed 07/7/18
356		Roofing Finishes	43 days	Tue 07/7/3	Tue 07/8/21
357		Key Date of Section 7 of the Works	1 day	Wed 07/8/29	Wed 07/8/29
358		Section 8 - All Remaining Works	239 days	Thu 07/4/26	Mon 08/1/28
359		E&M installation (by Others)	157 days	Thu 07/4/26	Thu 07/10/25
360		External Cable Duct, Drainage & Catchpit	55 days	Fri 07/10/19	Thu 07/12/20
361		Construction of Boundary Wall	58 days	Fri 07/10/19	Mon 07/12/24
362		Demolition of Existing Boundary Wall	7 days	Tue 07/12/25	Tue 08/1/1
363		Road Paving	21 days	Tue 07/12/25	Thu 08/1/17
364		Testing and Commissioning (by Others)	80 days	Wed 07/8/15	Thu 07/11/15
365		Connection to MH F2	7 days	Fri 07/11/16	Fri 07/11/23
366		Connection to MH1	7 days	Fri 07/11/16	Fri 07/11/23
367		Demolition of existing pumping pit	7 days	Sat 07/11/24	Sat 07/12/1
368		Grouting for Existing Sewer & Manhole	30 days	Mon 07/12/3	Fri 08/1/4
369		Landscaping	10 days	Sat 08/1/5	Wed 08/1/16
370		Establishment works	10 days	Thu 08/1/17	Mon 08/1/28
371		Key Date of Section 8 of the Works	1 day	Sat 07/11/24	Sat 07/11/24

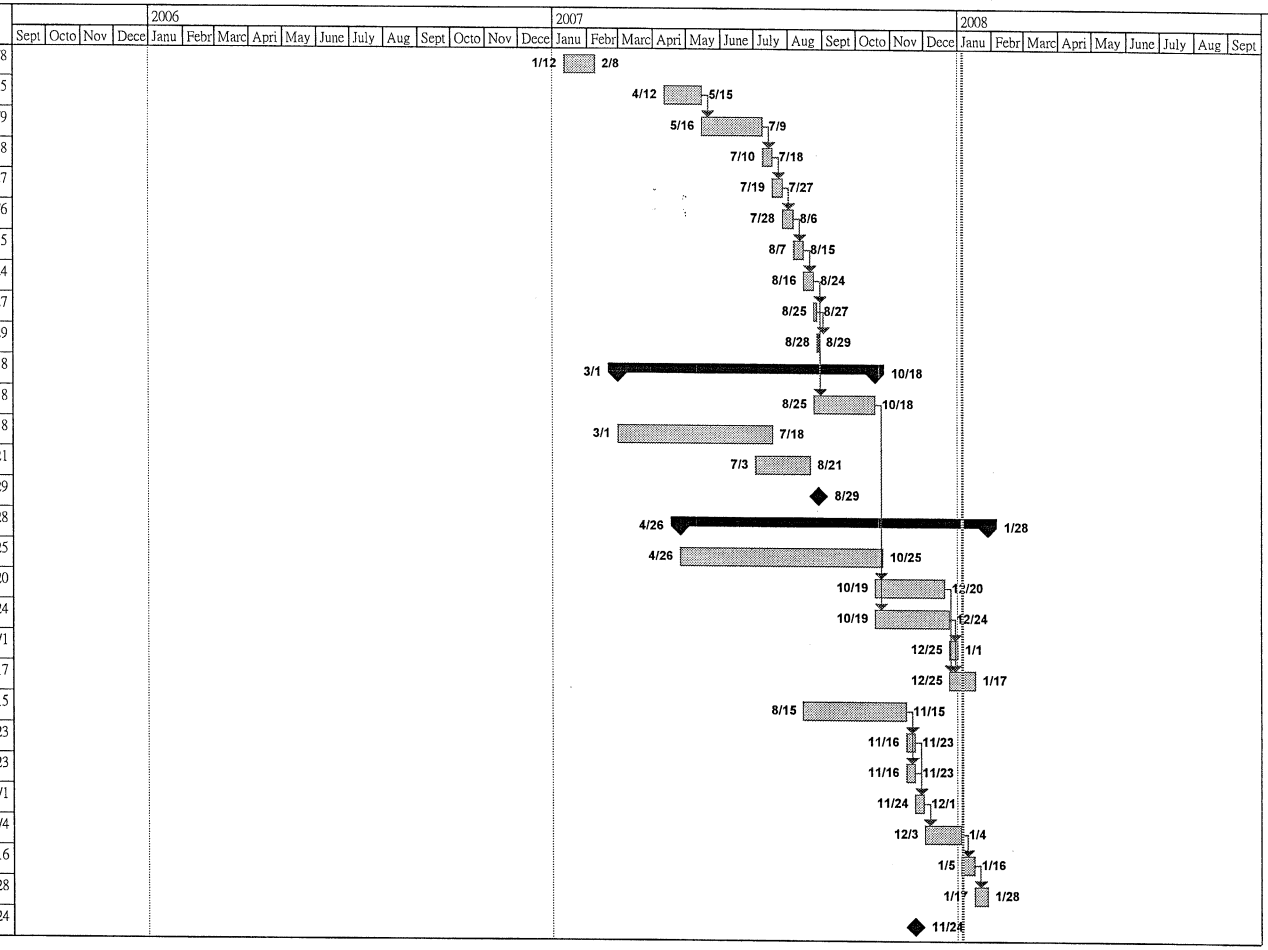

Date: Sat 08/1/5

Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks	
Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary	
