Proposed Comprehensive Development at Wo Shang Wai Yuen Long

Monthly EM&A Report for February 2014 (Rev A)

March 2014

Heng Shung Construction Co. Ltd.

Mott MacDonald

Proposed Comprehensive Development at Wo Shang Wai Yuen Long

Monthly EM&A Report for February 2014 (Rev A)

March 2014

Heng Shung Construction Co. Ltd.

Mott MacDonald, 20/F AIA Kowloon Tower, Landmark East, 100 How Ming Street, Kwun Tong, Kowloon, Hong Kong
T +852 2828 5757 **F** +852 2827 1823 w **W** www.mottmac.com

Pursuant to Condition 4.5 of Environmental Permit No. EP-311/2008/D, this Monthly EM&A Report for February 2014 has been reviewed, certified by Environmental Team Leader (ETL) and verified by the Independent Environmental Checker (IEC).

Certified by:

Terence Kong
Environmental Team Leader (ETL)
Mott MacDonald Hong Kong Ltd.

Date 14 March 2014

Verified by:

David Yeung
Independent Environmental Checker (IEC)
ENVIRON Hong Kong Limited

Date 14 March 2014

Contents

Chapter	Title	Page
Executive Summary		i
1	Introduction	1
1.1	Background	1
1.2	Project Organization	1
1.3	Environmental Status in the reporting period	1
1.4	Summary of EM&A Requirements	2
2	Impact Monitoring Methodology	4
2.1	Introduction	4
2.2	Air Quality	4
2.3	Construction Noise	7
2.4	Water Quality	9
2.5	Ecology	12
2.6	Landscape and Visual	13
3	Monitoring Results	17
3.1	Impact Monitoring Schedule	17
3.2	Results of Impact Monitoring	17
4	Ecological Monitoring	23
4.1	Monitoring of Birds	23
4.2	Monitoring of Herpetofauna	23
4.3	Monitoring of Dragonflies and Butterflies	23
4.4	Monitoring of Mammals	23
4.5	Monitoring of Water Quality	24
4.6	Management Activities	24
4.7	Summary	24
5	Landscape and Visual	25
5.1	Site Inspections	25
5.2	Construction Phase Audit Summary	25
6	Environmental Site Inspection and Audit	28
6.1	Site Inspection	28
6.2	Solid and Liquid Waste Management Status	28
6.3	Status of Environmental Licenses and Permits	28
6.4	Recommended Mitigation Measures	29
7	Report on Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions	30

7.1 Record on Non-compliance of Action and Limit Levels 30
7.2 Record on Environmental Complaints received 31
7.3 Record on Notifications of Summons and Successful Prosecution 32
7.4 Review of Reasons for and Implications of Non-compliance, Complaints, Summons and Prosecutions 32
7.5 Follow-up Actions Taken 34
7.6 Cumulative Statistics for Complaints, Notifications of Summons and Successful Prosecutions 35

8 Future Key Issues 36
8.1 Site Preparatory Works and Construction Works for the Coming Month 36
8.2 Key Issues for the Coming Months 36
8.3 Monitoring Schedule for the Coming Month 36
8.4 Conclusions and Recommendations 38

Tables

Table 1.1: Summary of Impact EM&A Requirements 2
Table 1.2: Environmental Monitoring and Audit Schedule for February 2014 3
Table 2.2: Air Monitoring Stations 4
Table 2.3: TSP Monitoring Equipment 5
Table 2.4: Noise Monitoring Parameters, Frequency and Duration 7
Table 2.5: Noise Monitoring Stations 7
Table 2.6: Noise Monitoring Equipment 8
Table 2.7: Water Quality Monitoring Parameters, Frequency and Duration 9
Table 2.8: Water Quality Monitoring Stations 9
Table 2.9: Water Quality Monitoring Equipment 10
Table 2.10: Analytical Methods applied to Water Quality Samples 10
Table 2.11: Detection Limits for Water Quality Determinants 11
Table 2.12: Summary of Construction Phase Ecological Monitoring for the Wo Shang Wai Wetland Restoration Area (WRA) 12
Table 2.13: Construction and Operation Phase Audit Checklist 14
Table 2.14: Proposed Construction Phase Mitigation Measures 14
Table 2.15: Proposed Operation Phase Mitigation Measures 15
Table 3.1: Summary of 1-hour TSP Monitoring Results 17
Table 3.2: Summary of 24-hour TSP Monitoring Results 18
Table 3.3: Summary of Construction Noise Monitoring Results 18
Table 3.4: Summary of Water Quality Monitoring Results 19
Table 4.1: Summary of Ecological Monitoring in WRA and Survey Area 24
Table 5.1: Construction and Operation Phase Audit Summary 25
Table 6.1: Summary of Site Inspections and Recommendations 28
Table 6.2: Status of Environmental Submissions, Licenses and Permits 28
Table 7.1: Summary of Exceedances in Water Quality 30
Table 7.2: Statistics for Complaints, Notifications of Summons and Successful Prosecutions 35
Table 8.1: Tentative Environmental Monitoring and Audit Schedule for March 2014 37

List of Figures

Figure 1.1 General Layout Plan of the Project Site

Figure 2.1 Locations of Air Quality Monitoring Stations
Figure 2.2 Locations of Noise Monitoring Stations
Figure 2.3 Locations of Water Quality Monitoring Stations
Figure 4.1 Survey Area and Transect Walked

List of Appendices

Appendix A Project Organization Chart
Appendix B Tentative Construction Programme
Appendix C Action and Limit Levels for Construction Phase
Appendix D Event and Action Plan for Air Quality, Noise and Water Quality
Appendix E Calibration Certificates
Appendix F Graphical Plots of the Monitoring Results
Appendix G Weather Conditions during the Monitoring Period
Appendix H Ecological Monitoring Conducted
Appendix I Summary of Bird Surveys conducted
Appendix J Summary of Herpetofauna, Mammal and Insect Surveys Conducted
Appendix K Summary of Monitoring of Water Quality associated with Ecological Monitoring Conducted
Appendix L Environmental Mitigation Measures - Implementation Status

Executive Summary

Mott MacDonald Hong Kong Ltd. ("MMHK") has been commissioned by Heng Shung Construction Co. Ltd. to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit (EM&A) for both pre-construction and construction phases of the Proposed Comprehensive Development at Wo Shang Wai, Yuen Long.

This is the 45th EM&A report submitted under the Condition 4.5 of Environmental Permit No. EP-311/2008/D. This report summarises the findings on EM&A during the period from 1 to 28 February 2014.

Exceedance of Action and Limit Levels

There was no breach of Action or Limit levels for Air Quality (1-hr TSP and 24-hr TSP) and Noise level (as L_{eq}) in the reporting month.

During February 2014, some Action/Limit Level exceedances were observed at MP3 while no exceedance was observed at MP4, MP5 and MP6.

The summary of measured water quality is presented in **Section 3.2.3**.

Investigations have been carried out to identify the causes of exceedance. From investigation, the Contractor has implemented water quality mitigation measures as recommended in the EIA report. With external factors affecting the adjacent environments, such as natural variations, pond fish culture activities and rainfall, the exceedances were considered not due to the project construction works.

Implementation of Mitigation Measures

Site audits were carried out on 11, 18 and 25 February 2014 to confirm the implementation measures undertaken by the Contractor in the reporting month. The outcomes are presented in **Section 6** and the status of implementation of mitigation measures in the site is shown in **Appendix L**.

Record of Complaints

There was no new record of complaints received in the reporting month.

One environmental complaint received in January 2014 has been followed up by ET and its description is reproduced below for the sake of convenience.

In January 2014, a formal complaint was made to the Environmental Protection Department (EPD) on dust impact at Palm Springs, Yuen Long. The complaint concerned suspected dust emissions from the Wo Shang Wai construction site. The ET received the formal complaint on 24 January 2014 via email from EPD. From ET's investigation conducted into the complaint, air quality mitigation measures as recommended in the Implementation Schedule of the EM&A Manual have been implemented by Contractor to minimise the air quality nuisance arising from the site activities. Nevertheless, such measures can be enhanced and recommendations were provided to the Contractor to further enhance the dust suppression within the site.

Record of Notification of Summons and Successful Prosecution

There was no record of Notification of summons and successful prosecution in the reporting month.

Reporting Changes

There was no reporting change in the reporting month.

Future Key Issues

The major site works scheduled to be commissioned in the coming three months include site formation, foundation work and pond drainage management in the Wetland Restoration Area (to lower the water level and remove unwanted species in the pond). Potential environmental impacts due to the construction activities, including air quality, noise, water quality, ecology and landscape and visual, will be monitored.

Environmental mitigation measures will be implemented on site as recommended and weekly site audits will be carried out to ensure that the environmental conditions are acceptable.

1 Introduction

1.1 Background

In March 2005, the Project Proponent, Profit Point Enterprises Limited, acquired the development site at Wo Shang Wai in Yuen Long. An Environmental Impact Assessment (EIA) was then carried out and approved under the EIA Ordinance (EIAO), and the Environmental Permit (EP-311/2008) for construction of the comprehensive development in Wo Shang Wai was first granted by EPD on 9 September 2008 and has been subsequently varied, with the current version (EP-311/2008/D) issued by EPD on 20 March 2013.

The Project involves the residential development and associated infrastructure and wetland restoration area and linear landscape area. The construction works under the Environmental Permit commenced on 12 May 2010. The site formation construction works of the Wetland Restoration Area (hereafter WRA) were completed on 15 November 2010, while the 30-month establishment period of the WRA was concluded in August 2012 – this indicated that planting works as scheduled in the approved Wetland Restoration and Creation Scheme (WRCS; Nov 2009) was complete, except along the western and southern boundary where the planting is affected by the existing site boundary and noise barrier, and for which a Variation to Environmental Permit (EP-311/2008/C) to defer planting at the location was approved. The current valid EP (EP-311/2008/D) includes specific mitigation measures to minimise certain identified noise impacts during the operation phase.

Mott MacDonald Hong Kong Ltd. ("MMHK") has been commissioned by the Contractor, Heng Shung Construction Co. Ltd., to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit (EM&A) for both pre-construction and construction phases of the Proposed Comprehensive Development at Wo Shang Wai, Yuen Long.

According to the EP Condition 4.5, the monthly EM&A Report shall be submitted to the Director within two weeks after the end of the reporting month. This report summarises the findings during the period from 1 to 28 February 2014.

1.2 Project Organization

The organisation chart and lines of communication with respect to the on-site environmental management structure together with the contact information of the key personnel are shown in **Appendix A**.

1.3 Environmental Status in the reporting period

During the reporting month, construction works of the Project undertaken include:

- Site formation
- Foundation work
- Pond drainage management in the Wetland Restoration Area (to lower the water level and remove unwanted species in the pond)

The Construction Works Programme of the Project is provided in **Appendix B**. The general layout plan of the Project site is shown in **Figure 1.1**.

1.4 Summary of EM&A Requirements

The EM&A programme requires environmental monitoring of air quality, noise, water quality, ecology and landscape and visual as specified in the approved EM&A Manual.

A summary of impact EM&A requirements is presented in **Table 1.1** below:

Table 1.1: Summary of Impact EM&A Requirements

Parameters	Descriptions	Locations	Frequencies
Air Quality	24-Hour TSP	ASR1, ASR2A, ASR3, ASR4	Once every 6 days
	1-Hour TSP	ASR1, ASR2A, ASR3, ASR4	3 times every 6 days
Noise	L_{eq}, 30min	NSR1, NSR3, NSR5, NSR7	Weekly
Water Quality	Dissolved Oxygen (DO), temperature, pH, suspended solids (SS) and Biological Oxygen Demand (BOD)	MP1 to MP6	3 days per week
Ecology	Birds	Within the Project Area and Assessment Area of 500m	Weekly
	Dragonflies and Butterflies	Within the Project Area and Assessment Area of 500m	Once per month during Mar and Sep to November, and twice per month during Apr to Aug
	Herpetofauna	Within the Project Area and Assessment Area of 500m	Once per month during Apr to Nov
	Water quality of Wetland Restoration Area (WRA)	WRA	After filling of WRA with water, monthly for in situ water quality and every size months (end of wet season and end of dry season) for laboratory testing
	Site Inspections	Within the Project Area and Assessment Area of 500m	Weekly
Landscape and Visual	Auditing of protection of existing trees, the transplanting of existing trees, the creation of new wetland, the planting of new trees and shrubs and other landscape and visual mitigation measures	CM1 to CM10 and OM1 to OM7 within the Project Area	Site inspections once every two weeks during construction phase; once every two months during operational phase

The Environmental Quality Performance Limits for air quality, noise and water quality are shown in **Appendix C**.

The Event and Action Plan for air quality, noise and water quality are shown in **Appendix D**.

The monitoring schedule for the reporting month is shown in **Table 1.2** below. (The Project site was closed for Lunar New Year holidays from 1 to 9 February 2014 inclusive, therefore no air and noise monitoring was conducted in the week commencing Monday 3 February 2014.)

Table 1.2: Environmental Monitoring and Audit Schedule for February 2014

Environmental Monitoring and Audit Schedule for Feb 2014

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1 The second day of Lunar New Year
2	3 The fourth day of Lunar New Year	4 **Bird** Water	5	6 Water	7	8 Water
9	10 Water	11 **Bird** 24-hr TSP 1-hr TSP Noise Monitoring *	12 Water	13	14 Water **Landscape** @	15
16	17 Water 24-hr TSP 1-hr TSP Noise Monitoring	18 **Bird** *	19 Water	20	21 Water 24-hr TSP 1-hr TSP **Water Quality (Ecology)**	22
23	24 Water	25 **Bird**	26 Water *	27 24-hr TSP 1-hr TSP Noise Monitoring	28 Water **Water Quality (Ecology)**	

* Site Audit by Mott MacDonald (MM)

@ Report Submission (Monthly EM&A Report)

Ecological Surveys & Landscape Audits indicated in **bold font**

2 Impact Monitoring Methodology

2.1 Introduction

For air quality, construction noise and water quality, ecology, landscape and visual monitoring methodology, including the monitoring locations, monitoring equipment used, monitoring parameters, and frequency and duration, etc, are detailed in this Chapter.

2.2 Air Quality

2.2.1 Monitoring Parameters, Frequency and Duration

In accordance with the EM&A Manual, 1-hour and 24-hour TSP levels monitoring are to be conducted during the construction phase. **Table 2.1** summarizes the monitoring parameters, frequency and duration of air quality monitoring.

Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
ASR1, ASR2A, ASR3 & ASR4	24-hour TSP	At least once in every six-days
	1-hour TSP	3 times every six-days

2.2.2 Monitoring Locations

The four air quality monitoring stations were established in the EM&A manual and were slightly adjusted during the baseline monitoring phase. Locations of the agreed air quality monitoring stations are listed in **Table 2.2** and as shown in **Figure 2.1**.

Table 2.2: Air Monitoring Stations

Monitoring Stations	Locations
ASR1	Works Site Boundary
ASR2A	At the rooftop of refuse collection point, which is located at the southwest of the project area
ASR3	At the commercial centre at Palm Springs, which is located at the south of the project area
ASR4	Works Site Boundary

2.2.3 Monitoring Equipment

Continuous 24-hour TSP air quality monitoring is conducted using High Volume Sampler (HVS) (Model: GMWS-2310 Accu-vol). The HVS meets all the requirements of the EM&A Manual. Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. **Table 2.3** summarizes the equipment used in the impact air quality monitoring.

Table 2.3: TSP Monitoring Equipment

Equipment	Model
24-hr TSP monitoring	
High Volume Sampler	GMWS 2310 Accu-vol
Calibrator	GMW 25
1-hr TSP monitoring	
Portable direct reading dust meter	AM510 SidePak Personal Aerosol Monitor Dust Trak 8520

2.2.4 Monitoring Methodology

2.2.4.1 24-hour TSP Monitoring

Installation

The HVS was installed in the vicinity of the air sensitive receiver. The following criteria were considered in the installation of the HVS.

- A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
- The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
- A minimum of two metres separation from walls, parapets and penthouse was required for rooftop sampler.
- A minimum of two metres separation from any supporting structure, measured horizontally was required.
- No furnace or incinerator flues or building vent were nearby.
- Airflow around the sampler was unrestricted.
- The sampler has been more than 20 metres from any drip line.
- Permission was obtained to set up the samplers and to obtain access to the monitoring stations.
- A secured supply of electricity is needed to operate the samplers.

Preparation of Filter Papers

- Glass fibre filters, were labelled and sufficient filters that were clean and without pinholes were selected.
- All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C with relative humidity (RH) < 50 % and was not variable by more than ±5 %. A convenient working RH was 40 %.

Field Monitoring

- The power supply was checked to ensure the HVS works properly.
- The filter holder and the area surrounding the filter were cleaned.
- The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
- The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
- The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges.
- The shelter lid was closed and was secured with the aluminium strip.
- The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
- A new flow rate record sheet was set into the flow recorder.
- The flow rate of the HVS was checked and adjusted at around 1.1 m^3/min. The range specified in the EM&A Manual was between 0.6-1.7 m^3/min.
- The programmable timer was set for a sampling period of 24 hrs + 1 hr, and the starting time, weather condition and the filter number were recorded.
- The initial elapsed time was recorded.
- At the end of sampling, the sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
- It was then placed in a clean plastic envelope and sealed.
- All monitoring information was recorded on a standard data sheet.
- Filters were sent to a HOKLAS accredited laboratory for analysis.

Maintenance and Calibration

- The HVS and its accessories are maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVSs were calibrated at two-month intervals.
- Calibration records for HVSs are shown in **Appendix E**.

2.2.4.2 1-hour TSP Monitoring

Field Monitoring

The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

- Set POWER to "ON", push BATTERY button, make sure that the meter's indicator is in the range with a red line and allow the instrument to stand for about 3 minutes (Then, the air sampling inlet has been capped).
- Push the knob at MEASURE position.
- Push "O-ADJ" button. (Then meter's indication is 0).
- Push the knob at SENSI ADJ position and set the meter's indication to S value described on the Test Report using the trimmer for SENSI ADJ.
- Pull out the knob and return it to MEASURE position.
- Push "START" button.

Maintenance and Calibration

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are shown in **Appendix E**.

2.3 Construction Noise

2.3.1 Monitoring Parameters, Frequency and Duration

Following the requirements in the EM&A Manual for noise, noise monitoring has to be carried out during the construction phase. Continuous noise monitoring for the A-weighted levels L_{eq}, L_{10} and L_{90} is undertaken once per every week.

Table 2.4 summarizes the monitoring parameters, frequency and duration of air quality monitoring.

Table 2.4: Noise Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
NSR1, NSR3, NSR5, NSR7	L_{eq}, L_{90} & L_{10}	Once every week

2.3.2 Monitoring Locations

The four noise quality monitoring stations were established in the EM&A manual and were slightly adjusted during the baseline monitoring phase. Locations of the agreed noise quality monitoring stations are listed in **Table 2.5** and as shown in **Figure 2.2**.

Table 2.5: Noise Monitoring Stations

Monitoring Stations	Locations	Type of measurement

Monitoring Stations	Locations	Type of measurement
NSR1	Noise monitoring equipment was set up near the boundary wall at Palm Springs.	Free-field
NSR3	The monitoring station was located next to the guard house at Palm Springs.	Facade
NSR5	The monitoring station was located within the work site boundary.	Free-field
NSR7	The monitoring station was located near the boundary wall of the house of Mai Po San Tsuen.	Free-field

2.3.3 Monitoring Equipment

Integrating Sound Level Meter will be used for noise monitoring. It is a Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They comply with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 2.6** summarizes the noise monitoring equipment model being used.

Table 2.6: Noise Monitoring Equipment

Monitoring Stations	Equipment Model	
	Integrating Sound Level Meter	Calibrator
NSR1	Rion NL-52	Rion NC-73
NSR3		
NSR5		
NSR7		

2.3.4 Monitoring Methodology

Field Monitoring

- The Sound Level Meter was set on a tripod at a height of at least 1.2 m above the ground.
- Façade and free-field measurements were made at the monitoring locations.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:

  - frequency weighting: A

  - time weighting: Fast

  - time measurement: 30 minutes intervals (between 07:00 and 19:00)

- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid has to be repeated after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq}, L_{10} and L_{90} were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.

Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix E**.

2.4 Water Quality

2.4.1 Monitoring Parameters, Frequency and Duration

In accordance with the requirements in the EM&A Manual for water quality, water quality parameters including Dissolved Oxygen (DO), temperature, pH, turbidity, suspended solids (SS) and Biochemical Oxygen Demand (BOD) have to be monitored at designated monitoring stations during construction of the Project. DO, temperature and pH were measured in-situ whereas SS and BOD were analysed in a laboratory. The measurements should be taken at all designated monitoring stations, three days per week. The interval between any two sets of monitoring was not less than 36 hours. **Table 2.7** summarizes the monitoring parameters, frequency and duration of water quality monitoring.

Table 2.7: Water Quality Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
MP1, MP2, MP3, MP4, MP5 & MP6	DO, temperature, pH, SS, turbidity, BOD	Three days every week

2.4.2 Monitoring Locations

The six water quality monitoring stations were established in the EM&A manual. Locations of the agreed water quality monitoring stations are listed in **Table 2.8** and as shown in **Figure 2.3**..

Table 2.8: Water Quality Monitoring Stations

Monitoring Stations	Easting	Northing
MP1	838 730.50	822 862.25
MP2	838 933.26	823 247.41
MP3	839 107.17	823 596.84

Monitoring Stations	Easting	Northing
MP4	839 286.14	823 638.55
MP5	839 134.35	823 722.99
MP6	839 063.02	823 842.25

2.4.3 Monitoring Equipment

The Water Quality Monitoring Equipment and Analytical Methods applied to Water Quality Samples are given in **Table 2.9** and **Table 2.10** respectively. Details of which are discussed below.

Table 2.9: Water Quality Monitoring Equipment

Equipment	Model	Equipment/Serial Number
Conductivity, Dissolved oxygen, pH, Salinity and Temperature Measuring Meter	YSI Professional Plus	09K100735
Turbidity Meter	Hach 2100Q	11050C001264
Global Positioning System (GPS)	Garmin eTrex Vista	ENO 007

Table 2.10: Analytical Methods applied to Water Quality Samples

Determinant, unit	Standard Method
Total Suspended Solids, mg/L	In house method based on APHA 2540D; ALS Method Code: EA-025
Biochemical Oxygen Demand (BOD), mg/L	In house method based on APHA 5210B; ALS Method Code: EP-030

All in-situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use.

Dissolved Oxygen (DO), temperature and pH measuring equipment

A portable, weatherproof multiparameter instrument (YSI Professional Plus) was used in the monitoring. It can be capable for measuring dissolved oxygen (DO), pH, and temperature simultaneously with the following limits:

- a dissolved oxygen level in the range of 0-50 mg/L and 0-500 % saturation;
- a temperature of -5 to 45 degree Celsius; and
- pH value of 0-14 with 0.1 as the base unit.

Turbidity Measurement Instrument

Portable and weatherproof turbidity meter (HACH model 2100Q) was used during impact monitoring. It has a photoelectric sensor capable of measuring turbidity between 0-1000 NTU. Response of the sensor was checked with certified standard turbidity solutions before the start of measurement.

Global Positioning System

A hand-held GPS navigator (Garmin eTrex Vista) was used to identify the designated monitoring stations prior to water sampling.

Suspended Solids and BOD Measurements (Sample Containers and Storage)

Water samples for SS analysis were stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen), delivered to the laboratory, and analysed as soon as possible after collection. Analysis was carried out in a HOKLAS accredited laboratory.

2.4.4 Detection Limit

The limits of detection for the in-situ and laboratory measurements are shown in **Table 2.11**.

Table 2.11: Detection Limits for Water Quality Determinants

Determinant	Limit of Detection
Dissolved Oxygen	0.1 mg/L
Temperature	0.1 degree Celsius
pH	0.01 unit
Turbidity	0.1 NTU
Suspended Solids	1 mg/L
BOD	2 mg/L

2.4.5 Monitoring Methodology

In situ measurement

All pH meters, DO/temperature meters had been checked and calibrated prior to use. Standard buffer solution of at least two pH levels (either pH 4 and pH 7, or pH 7 and pH 10) had been used for calibration of the instrument before and after use.

DO meters had been calibrated by a laboratory accredited under HOKLAS or any other international accreditation scheme, and subsequently re-calibrated at three-monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes had been checked with certified standard solutions before each use. Wet bulb calibrations for all DO meters had been carried out before measurement at each monitoring location. For the on-site calibration of field equipment, BS 127:1993, "Guide to field and on-site test methods for the analysis of waters" had been observed.

Measurements shall be at three water depths, namely, 1m below water surface, mid-depth and 1m above stream bed/pond bed, except where the water depth less that 6m, the mid-depth station maybe omitted. Should the water depth be less than 3m, only the mid-depth station will be monitored.

Replicates in-situ measurements and samples collected from each independent monitoring event are required for all parameters to ensure a robust statistically interpretable dataset.

Water Samples Preparation and Analysis

For collection of water sampling within the water courses, a 500ml clean plastic beaker was used. After collection, the water samples were stored in high-density polythene bottles. The sample container was rinsed with a portion of the water sample. The water sample was then transferred to the container, labelled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4°C. The water samples were then delivered to a local HOKLAS-accredited laboratory (ALS) on the same day for analysis.

The testing methods of testing parameters as recommended by EIA or required by EPD, with the QA/QC results are in accordance with the requirement of HOKLAS or international accredited scheme.

The calibration certificates for equipment used for in-situ monitoring of water quality are attached in **Appendix E**.

2.5 Ecology

2.5.1 Monitoring Parameters, Frequency and Duration

Target species and certain other fauna will be monitored within the Project Area and Assessment Area during the wetland and residential construction phase. This will be important to ensure that any unexpected events or impacts either on- or off-site are quickly identified so that remedial action can be taken. The groups to be monitored and frequency of monitoring are shown in **Table 2.12**.

Table 2.12: Summary of Construction Phase Ecological Monitoring for the Wo Shang Wai Wetland Restoration Area (WRA)

Species / Parameter	Construction Phase Ecological Monitoring
Birds	Weekly (including Assessment Area).
Dragonflies and Butterflies	Once per month during March and September to November, and twice per month during April to August.
Herpetofauna	Once per month during April to November.
Water Quality	After filling of WRA with water, monthly for *in situ* water quality and every six months (end of the wet season and end of the dry season) for laboratory testing.
Site Inspections	Weekly.

2.5.2 Monitoring Locations and Methodology

Ecological monitoring locations during construction phase are shown in **Figure 4.1** and the methodology for ecological monitoring is detailed in **Section 4**.

2.6 Landscape and Visual

2.6.1 Monitoring Parameters, Frequency and Duration

All measures undertaken by both the Contractor and the specialist Landscape Sub-Contractor during the construction phase and first year of the operational phase shall be audited by a Registered Landscape Architect, as a member of the ET, on a regular basis to ensure compliance with the intended aims of the measures. Site inspections should be undertaken at least once every two weeks throughout the construction period and once every two months during the operational phase.

The broad scope of audit is detailed below but should also be undertaken with reference to the more specific checklist provided in **Table 2.13** below. Operational phase auditing will be restricted to the last 12 months of the establishment works of the landscaping proposals and thus only the items below concerning this period are relevant to the operational phase.

- The extent of the agreed works area should be regularly checked during the construction phase. Any trespass by the Contractor outside the limit of the works, including any damage to existing trees and woodland shall be noted;
- The progress of the engineering works should be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken;
- All existing vegetation, streams and other features within the study area which are not directly affected by the works are retained and protected;
- The methods of protecting existing vegetation proposed by the Contractor are acceptable and enforced;
- Preparation, lifting transport and re-planting operations for any transplanted trees;
- The layout, design and construction of buildings conforms to requirements specified in the EIA report;
- All landscaping works are carried out in accordance with the EIA recommendations and with specifications;
- The planting of new trees, shrubs, groundcover, climbers, grasses and other plans, together with the replanting of any transplanted trees are carried out properly and within the right season;
- All necessary horticultural operations and replacement planting are undertaken throughout the Establishment Period to ensure the healthy establishment and growth of both transplanted trees and all newly establishment plants.

Table 2.13: Construction and Operation Phase Audit Checklist

Area of Works	Items to be Monitored
Works Area	Check the extent of the Works to ensure that the Works Area is not exceeded
Protection of all trees and woodland blocks to be retained	Identification and demarcation of trees / vegetation to be retained, erection of physical protection (e.g. fencing), monitoring against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Streams	Ensure no run-off into existing streams
Clearance of existing vegetation	Identification and demarcation of trees / vegetation to be cleared, checking of extent of works to minimize damage, monitoring of adjacent areas against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Transplanting of trees	Identification and demarcation of trees / vegetation to be transplanted, monitoring of extent of pruning / lifting works to minimize damage, timing of operations implementation of all stages of preparatory and translocation works, and maintenance of transplanted vegetation, etc.
Topsoil stripping	Ensuring existing topsoil is stripped and stored under recognized good practice and is hydroseeded and regularly turned to prevent anaerobic conditions
New buildings	Ensure that building finishes accord with mitigation proposals with regard to colour and albedo.
Boundaries	Ensuring hoarding are erected as required
Noise Barrier	Ensure noise barrier design accords with the mitigation proposals with regard to location, materials and finishes.
Night-time lighting	Ensuring night-time lighting is directional, hooded and shielded away from VSRs
Plant supply	Monitoring of operations relating to the supply of specialist plant material (including the collecting, germination and growth of plants from seed) to ensure that plants will be available in time to be used within the construction works.
Landscape and wetland treatments generally	Check that wetland, and hard / soft landscape designs conform to intent of mitigation measures and agreed designs
Soiling, planting, etc.	Monitoring of implementation and maintenance of soiling and planting works against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Establishment Works	Monitoring of implementation of maintenance operation during Establishment Period

2.6.2 Monitoring Locations

The monitoring locations should check against the mitigation measures proposed under the approved Environmental Impact Assessment, which are summarised as follows in **Table 2.14** and **Table 2.15**:

Table 2.14: Proposed Construction Phase Mitigation Measures

ID No.	Landscape and Visual Mitigation Measure
CM1	The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape.
CM2	Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colours, to screen Works.

ID No.	Landscape and Visual Mitigation Measure
CM3	Reduction of construction period to practical minimum.
CM4	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where the soil material meets acceptable criteria and where practical. The Contract Specification shall include storage and reuse of topsoil as appropriate.
CM5	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone).
CM6	Advance screen planting to noise barriers.
CM7	Control night-time lighting and glare by hooding all lights.
CM8	Ensure no run-off into streams adjacent to Project Area.
CM9	Protection of existing trees on boundary of project area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at S16 and Tree Removal Application stage).
CM10	Trees unavoidably affected by the works shall be transplanted where practical. Trees should be transplanted straight to their destinations and not held in a nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.

Table 2.15: Proposed Operation Phase Mitigation Measures

ID No.	Landscape Mitigation Measure
OM1	Compensatory Tree Planting for all felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.
OM2	A continuous belt of screen planting along southern perimeter of project area with fast growing tree species. At least 450 trees capable of reaching a height > 10m within 10 years should be planted. Planting of the belt of trees shall be carried out as advance works ahead of other site formation and building works.
OM3	Maximise soft landscape and amenity water bodies in residential areas of the development. Approximately 750 trees (of Heavy Standard size) should be planted. Where space permits, roadside berms should be created. Street trees should be of species that reach a mature height of no less than 15m.
OM4	Maximise freshwater habitat wetland creation consistent with achieving other parameters. Minimum 4.74 ha to be provided. Wetlands must have natural edge profiles with >1m wide emergent zone. No access to the wetland by residents and all wetlands must be screened from residential development by a continuous tree screen at interface with residential development or earth mounding such that disturbance is minimised. Implementation of the wetland shall be carried out as advance works.
OM5	Use appropriate (visually unobtrusive and non-reflective) building materials and colours in built structures.

ID No.	Landscape Mitigation Measure
OM6	During detailed design, refine building layout to create a min. 10m wide gap between buildings north of Wo Shang Wai pond and also two min. 10m wide gaps in the row of buildings adjacent to Royal Palms.
OM7	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimise unnecessary light spill.

3 Monitoring Results

3.1 Impact Monitoring Schedule

Impact monitoring for air quality (dust), noise and water quality due to the construction work were undertaken during the reporting month in compliance with the EM&A manual in the reporting period. Regular site inspections were carried out on 11, 18 and 25 February 2014 in the reporting month to assess the compliance with environmental requirements. (The Project site was closed for Lunar New Year holidays from 1 to 9 February 2014 inclusive, therefore no air and noise monitoring was conducted in the week commencing Monday 3 February 2014.)

3.2 Results of Impact Monitoring

3.2.1 Air Quality Monitoring

3.2.1.1 1-hr TSP

Results of 1-hour TSP at the four monitoring locations are summarised in **Table 3.1**. Graphical plots of the monitoring results are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.1: Summary of 1-hour TSP Monitoring Results

Monitoring Date	Start Time	1-hr TSP (μg/m^3)			Range (μg/m^3)	Action Level (μg/m^3)	Limit Level (μg/m^3)
		1st Result	2nd Result	3rd Result			
ASR1							
11-Feb-14	13:15	101	112	104	89-139	378	500
17-Feb-14	13:20	119	120	106			
21-Feb-14	13:20	89	105	114			
27-Feb-14	13:30	115	134	139			
ASR2A							
11-Feb-14	12:47	104	108	111	71-118	357	500
17-Feb-14	12:49	118	115	107			
21-Feb-14	12:48	81	74	71			
27-Feb-14	12:15	99	96	84			
ASR3							
11-Feb-14	12:34	112	106	114	91-124	358	500
17-Feb-14	12:36	115	124	120			
21-Feb-14	12:35	117	99	105			
27-Feb-14	12:37	91	102	100			
ASR4							
11-Feb-14	13:02	122	104	116	104-141	372	500
17-Feb-14	13:10	141	136	130			
21-Feb-14	13:02	115	112	105			
27-Feb-14	16:02	115	106	117			

3.2.1.2 24-hr TSP

Results of 24-hour TSP at the four monitoring locations are summarised in **Table 3.2**. Graphical plots of the monitoring results are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.2: Summary of 24-hour TSP Monitoring Results

Monitoring Date	Monitoring Results ($\mu g/m^3$)	Range ($\mu g/m^3$)	Action Level ($\mu g/m^3$)	Limit Level ($\mu g/m^3$)
ASR1				
11-Feb-14	88	88-96	226	260
17-Feb-14	94			
21-Feb-14	90			
27-Feb-14	96			
ASR2A				
11-Feb-14	99	88-99	213	260
17-Feb-14	88			
21-Feb-14	89			
27-Feb-14	92			
ASR3				
11-Feb-14	102	85-102	205	260
17-Feb-14	85			
21-Feb-14	91			
27-Feb-14	89			
ASR4				
11-Feb-14	84	84-90	237	260
17-Feb-14	90			
21-Feb-14	90			
27-Feb-14	85			

No exceedance of 1-hour and 24-hour TSP (Action or Limit Level) was recorded in the reporting period.

3.2.2 Construction Noise Monitoring

The construction noise monitoring results are summarized in **Table 3.3**. Graphical plots of the monitoring data are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**..

Table 3.3: Summary of Construction Noise Monitoring Results

Monitoring Date	Start Time	Mean & Range of Noise Levels, dB(A)			Limit Level for L_{eq} (dB)
		L_{eq}	L_{10}	L_{90}	

Monitoring Date	Start Time	Mean & Range of Noise Levels, dB(A)			Limit Level for L_{eq} (dB)
		L_{eq}	L_{10}	L_{90}	
NSR1					> 75
11-Feb-14	15:39	52	55	48	
17-Feb-14	15:39	52	56	50	
27-Feb-14	15:23	55	58	49	
NSR3					
11-Feb-14	14:57	55	58	47	
17-Feb-14	14:56	58	60	47	
27-Feb-14	14:46	52	56	46	
NSR5					
11-Feb-14	13:20	59	62	54	
17-Feb-14	13:26	57	59	56	
27-Feb-14	13:37	61	59	58	
NSR7					
11-Feb-14	14:06	66	69	57	
17-Feb-14	14:09	67	71	59	
27-Feb-14	14:09	66	68	59	

No exceedance (Action/Limit Level) of construction noise was recorded in the reporting period.

3.2.3 Water Quality Monitoring

The water quality monitoring results are summarized in **Table 3.4**. Graphical plots of the monitoring data are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.4: Summary of Water Quality Monitoring Results

Monitoring Date	Temp (°C)	pH	Dissolved Oxygen (DO) (mg/L)	DO (%)	Turbidity (NT)	BOD (mg/L) (1)	Suspended Solids (mg/L)
MP3							
04/02/2014	22.4	7.4	**5.1**	62.8	30.8	4	16
06/02/2014	24.3	7.5	**6.2**	75.8	38.3	2	14
08/02/2014	24.3	**7.6**	**5.8**	71.5	39.3	2.5	11
10/02/2014	13.1	7.5	9.5	90.6	23.1	6	16
12/02/2014	11.3	7.5	10.3	94.3	26.3	10	14
14/02/2014	11.8	7.5	9.3	86.2	27.6	4	6
17/02/2014	20.2	7.5	7.8	86.4	15.6	5	7
19/02/2014	14.1	7.5	9.5	92.3	20.5	8.5	10.5
21/02/2014	15.1	7.5	8.7	86.6	28.2	7	23
24/02/2014	21.1	7.4	7.9	88.7	17.9	9	25
26/02/2014	22.3	7.4	7.4	85.7	30.7	6.5	22.5

Monitoring Date	Temp (°C)	pH	Dissolved Oxygen (DO) (mg/L)	DO (%)	Turbidity (NT)	BOD (mg/L) (1)	Suspended Solids (mg/L)
28/02/2014	19.3	7.4	8.4	91.1	**80.3**	7.5	**88**
Action Level	-	<5.5 or >7.5	<6.85	-	>64	-	>65
Limit Level	-	<4.0 or >8.0	<6.65	-	>67	-	>66
MP4							
04/02/2014	22.1	7.5	6.0	73.2	44.9	4.5	41.5
06/02/2014	23.8	7.4	6.3	76.8	32.5	<2	15.5
08/02/2014	22.6	7.5	6.0	73.2	33.7	3	11
10/02/2014	13.5	7.4	9.0	85.9	26.7	2	20.5
12/02/2014	10.5	7.4	10.6	95.3	26.9	2	10.5
14/02/2014	12.1	7.4	9.5	88.1	21.2	2	10
17/02/2014	19.9	7.4	8.2	90.2	17.8	<2	4
19/02/2014	13.5	7.4	9.1	87.6	28.2	3.5	13
21/02/2014	14.8	7.4	8.3	81.7	22.3	3	16.5
24/02/2014	20.9	7.4	7.8	87.5	18.9	2.5	20.5
26/02/2014	22.1	7.4	7.2	82.9	27.2	2	21.5
28/02/2014	19.1	7.4	8.5	91.1	32.5	2.5	19
Action Level	-	<5.5 or >7.5	<3.91	-	>60	-	>50
Limit Level	-	<4.0 or >8.0	<3.82	-	>64	-	>53
MP5							
04/02/2014	22.3	7.5	6.3	77.7	49.0	4	32.5
06/02/2014	23.6	7.5	5.4	67.3	36.7	2	10
08/02/2014	22.8	7.4	6.1	75.9	36.4	3	10.5
10/02/2014	13.6	7.4	8.7	83.4	28.1	2	21
12/02/2014	10.8	7.4	9.6	86.7	26.6	2	11.5
14/02/2014	12.5	7.4	8.9	83.9	21.5	2	10
17/02/2014	19.7	7.4	7.9	86.8	18.3	<2	4
19/02/2014	13.7	7.4	9.0	87.1	28.6	3	11.5
21/02/2014	14.9	7.4	8.4	83.3	23.1	3	13
24/02/2014	20.3	7.4	8.1	89.7	16.8	2	16
26/02/2014	21.8	7.4	7.5	86.5	30.1	<2	22.5
28/02/2014	18.8	7.4	8.3	89.5	30.7	2	19
Action Level	-	<5.5 or >7.5	<4.13	-	>81	-	>66
Limit Level	-	<4.0 or >8.0	<3.87	-	>84	-	>69
MP6							
04/02/2014	22.4	7.5	5.7	69.8	46.3	4	29
06/02/2014	23.5	7.5	5.4	66.9	32.3	2.5	12
08/02/2014	22.9	7.5	5.7	70.0	42.3	3.5	13.5

Monitoring Date	Temp (°C)	pH	Dissolved Oxygen (DO) (mg/L)	DO (%)	Turbidity (NT)	BOD (mg/L) (1)	Suspended Solids (mg/L)
10/02/2014	13.6	7.4	8.3	80.0	27.3	<2	15.5
12/02/2014	10.9	7.4	9.2	83.7	26.1	<2	10.5
14/02/2014	12.5	7.4	9.7	91.6	22.6	2	10
17/02/2014	19.6	7.4	7.5	82.1	18.9	<2	3.5
19/02/2014	13.8	7.4	8.4	81.1	28.2	3	13
21/02/2014	14.9	7.4	8.1	80.2	24.8	2.5	12
24/02/2014	20.3	7.4	7.2	79.9	16.2	2	17
26/02/2014	21.9	7.4	7.3	84.0	29.3	2	29.5
28/02/2014	18.6	7.4	7.8	83.1	29.6	2	19.5
Action Level	-	<5.5 or >7.5	<4.61	-	>94	-	>75
Limit Level	-	<4.0 or >8.0	<4.52	-	>96	-	>75

Notes:

(1) "<2 " : BOD value is too low to indicate (<2mg/L).

(2) Values **Bold** indicate Action Level exceedance.

(3) Values **Underlined and Bold** indicate Limit Level exceedance.

3.2.3.1 Exceedance Investigation and Findings

During February 2014, some Action/Limit Level exceedances were observed at MP3 while no exceedance was observed at MP4, MP5 and MP6. The Event and Action Plan in **Appendix D** was followed under these cases of exceedances.

From investigation, construction activities during the period of exceedance included mainly site formation and foundation work, as well as pond drainage management in the Wetland Restoration Area (to lower the water level and remove unwanted species in the pond). It was observed that the Contractor has implemented water quality mitigation measures as recommended in the EIA report, including the provision of temporary drainage facility and associated treatment facility. Sand bags are in place in the temporary drainage channel to enhance the desilting efficiency. The Contractor further enhanced the water quality mitigation measures by erecting several segments of rock bunds and installing a barrier at the discharge outlet to desilt and divert site runoff to sedimentation tanks and wastewater treatment facilities (Aquased), which will ensure all site runoff is treated to satisfactory quality before discharging into the northern ditches.

Exceedances of pH, DO, turbidity and SS at MP3

During the reporting month at MP3, exceedance of the Action/Limit Level of pH was observed on one monitoring date, while Limit Level exceedance of DO was recorded on three monitoring dates. Limit Level exceedance of turbidity and SS were both observed on one monitoring date. As understood, the fish pond near the site (represented by MP3) was being separated from the construction site by the WRA since November 2010, so the exceedances were not considered to be related to the construction activities. The exceedances of pH, DO, turbidity and SS may be due to external factors such as pond fish culture activities which were out of the control of the project.

Conclusion

As a result, the abovementioned exceedances are unlikely to be due to the construction works and therefore not considered to be related to the project.

4 Ecological Monitoring

4.1 Monitoring of Birds

This report documents surveys conducted in the Survey Area between 1 and 28 February 2014. The Wetland Restoration Area (WRA) is also surveyed as the area is accessible and site formation works for WRA has been completed. The updated survey transect is provided in **Figure 4.1**. Dates and ecological surveys conducted during this period are summarised in **Appendix H**.

Monitoring was undertaken following the survey methodology in the EM&A Manual. A transect was followed in the bird surveys (see **Figure 4.1**). All bird species were identified to species and all bird species of conservation importance and/or wetland dependent were enumerated and recorded to the habitats in which they were observed. Flying birds were not recorded unless they were foraging and/or associated with the habitat (such as swifts). Further, notable bird observations during other surveys were also recorded.

Bird surveys were conducted on a weekly basis. A total of 39 bird species were recorded in the Survey Area (excluding the WRA), 21 of which were species of conservation importance and/or wetland-dependence. Within the WRA, 38 bird species were recorded, 23 of which were species of conservation importance and/or wetland-dependent species, including two of the target species (i.e. Little Egret and Chinese Pond Heron) was recorded. The WRA continues to attract a number of species of conservation importance, including Eurasian Eagle Owl, *Bubo Bubo*, Northern Shoveler, *Anas clypeata* and Chinese Penduline Tit, *Remiz consobrinus*. These species are listed by Fellowes *et al*. as of "Regional Concern" in 2002.

4.2 Monitoring of Herpetofauna

No herpetofauna surveys were scheduled in the period. No amphibian species or reptile species were recorded in other surveys.

A summary of the survey findings is provided in **Appendix J**.

4.3 Monitoring of Dragonflies and Butterflies

No dragonfly and butterfly surveys were scheduled in the period.

A summary of the survey findings is provided in **Appendix J**.

4.4 Monitoring of Mammals

Monitoring of mammals was conducted concurrently with other surveys. No mammals were recorded in the Survey Area nor the WRA during regular survey and additional night search.

A summary of the survey findings is provided in **Appendix J**.

4.5 Monitoring of Water Quality

During the reporting period, water level of Cell 2 reached the action level. Monitoring data are presented in **Appendix K**.

4.6 Management Activities

4.6.1 Vegetation Management

Removal of exotic vegetation in all cells was undertaken; these included but not limited to *Ipomoes sp., Mikania sp., Mimosa sp., Pennisetum sp.* and *Typha sp*.

Vegetation management activities undertaken at the site primarily involved watering of plants, weeding and grass cutting.

4.6.2 Wildlife Management

Removal of Golden Apple Snail was undertaken on an "as-seen" basis.

All sighted Red Fire Ant nests were treated with approved pesticide.

4.7 Summary

Ecological monitoring during February 2014 was carried out according to the survey methodology and frequency outlined in the EM&A Manual.

Summary of survey findings is listed in **Table 4.1** below:

Table 4.1: Summary of Ecological Monitoring in WRA and Survey Area

Species	Survey Area (excluding WRA)	WRA
Birds (total)	39	38
Birds (of conservation importance and/or wetland-dependence)	21	23
Amphibians	0	0
Reptiles	0	0
Mammals	0	0
Odonates	0	0
Butterflies	0	0

Survey findings indicate that the ponds within the Survey Area supported numbers and diversity of wetland-dependent birds typical of fish pond areas. The WRA continues to attract wetland dependent fauna and serves as a buffer between the residential portion and the fishponds in the north.

5 Landscape and Visual

5.1 Site Inspections

The EM&A programme for Landscape and Visual impact due to the construction commenced in June 2010 and continued during the reporting period. Site inspections on Landscape and Visual impact were carried out on 7 February and 1 March 2014 to confirm the implementation of mitigation measures at construction stage.

5.2 Construction Phase Audit Summary

The audit was undertaken with references to the specific checklists provided in **Tables 2.13 – 2.15** and audit results are summarized as below:

Table 5.1: Construction and Operation Phase Audit Summary

Area of Works	Items to be Monitored
Works Area	The boundaries of the works area have been established on site in accordance with the contract documents and approved plans (EP), and the limit of current heavy construction activity is now confined to within the site hoardings (North side of the site / access road) and the noise barriers (other sides of the site). Minor works such as horticultural maintenance of the planting and transplanted trees, and boundary fence repair was proceeding along the Royal Palms – Palm Springs boundary. No construction works were observed to have exceeded the site boundaries. No construction was carried out at the wetland restoration area after 15 November 2010.
Protection of all trees and woodland blocks to be retained	Trees retained within the site along the northeast boundary, beside wetland restoration area, have been identified and protected by temporary protective fencing.
Streams	The works site is partly encircled by a berm / perimeter channel to intercept surface water and prevent it from washing off into any of the neighboring sites. Surface water is collected within the site in a temporary drainage channel. Gravels beds and barriers have been installed to filter site runoff, sedimentation ponds have been provided to enable primary treatment before discharge to mains drains.
Clearance of existing vegetation	Site clearance was completed prior to the commencement of construction.
Transplanting of trees	Tree transplanting has been completed, with the trees relocated to various points within the planting strip along the southern boundary of the site, outside the noise barrier. The trees continue to re-establish well.
Topsoil stripping	Suitable pond bund and soil material which had been excavated and stockpiled from the original site, has now been re-used within the landscape works. Dust suppression measures are active along all internal site access tracks.

New buildings	No new permanent buildings have yet been constructed on site.
Boundaries	Hoardings have been erected along most of the boundaries of the site. Installation of new screen fence between the future residential sites and the constructed wetland restoration areas is complete. Fence has been painted green to match with the surrounding vegetated environment.
Noise Barrier	Noise barriers have been installed along the southern and western boundaries of the site in accordance with the contract requirements. Their design complies with the mitigation requirements, with upper 6 to 7m portion of the barrier being made from a translucent material with green tinted (to match with the environment). Supporting GMS structure, likewise, has been painted green.
Night-time lighting	No night-time works were reported to have been carried out during the monitoring period
Landscape and wetland treatments generally	Continuous belt of screen planting along the southern and western boundaries of the site has been completed. The formation, soiling and water control structures of the wetland restoration area have been completed. The wetland areas are being established, with the ponds are being seasonally filled with rain water. Planting of areas around the WRA cells is complete. No construction was carried out at the wetland restoration area after 15 November 2010.
Soiling, etc.	The soiling for the advance planting strip has been completed. The soil placement and grading for each of the wetland restoration areas has been completed.
Plant supply	The plant material used in the Advance Planting Strip and in the WRA are all commonly available species and came from commercial sources. Transplanted reeds (*Phragmites australis*) at the wetland habitat came from the temporary holding nursery onsite.
Planting	The total number of trees that will reach a minimum of 10m in the advance planting strip meets the contract requirements. The tree species are all from the approved list. This planting should achieve the required screening effect within the required time period. Some of the trees that were identified as dead in previous month or having defects (i.e. extensive bark damage, cavities, fungal growths, etc.) still need to be replaced with new specimens. Some of the recently planted trees are still in poor condition, but are showing small signs of graduate improvement Seedling trees and shrubs, have been established at the margins of the wetland cells. Some additional fill-in planting has been undertaken.

Establishment Works	The advance planting, the compensatory planting and transplanted trees are generally being maintained by the landscape sub-contractor in accordance with the specification to ensure that the contract requirements are met, although treatment of damaged / defective trees needs urgent attention. Some of the trees that were identified as dead in previous month still need to be replaced with new specimens. Trees with significant defects (i.e. extensive bark damage, cavities, fungal growths, etc.) need to be replaced with new specimens. Growth of some trees and shrubs continues to be seriously affected by overhanging/ fallen trees on adjacent property. Removal of these overhanding / fallen trees needs to be undertaken immediately. Many trees are growing (and have become dependent for support) on the noise barrier frame, and are being deformed and damaged. Trees should either be physically separated from the structure, or the structure modified to avoid impacting on trees. Pruning of tall shrubs (e.g. *Ligustrum sinensis*) needs to be undertaken regularly. Removal of extensive growth of weeds and invasive climbers in the space behind screen noise barrier has been carried out, but clearance needs to be undertaken on a monthly basis as they may be inhibiting the advance planting. *Phragmites australis* reeds are now occupying up to 80% of the reed bed areas within the WRC (as per design), but have also spread to the non-reed bed areas and are out-competing the intended planting. Regular horticultural maintenance (grass cutting, weeding, watering etc.) in the shrubs and tree seedling areas around the WRA cells is being undertaken. The trees / shrubs planted along the northern site boundary are showing seasonal insect infestation again. Growth of shrubs / seedlings on the north side of WRA1 is still unsatisfactory.

6 Environmental Site Inspection and Audit

6.1 Site Inspection

The ET had carried out construction phase weekly site inspections on 11, 18 and 26 February 2014. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary. The key observations from site inspections and associated recommendations are summarized in **Table 6.1**.

Table 6.1: Summary of Site Inspections and Recommendations

Key Observations	ET Recommendation	Contractor's Responses / Action(s) Undertaken	Close-out (Date)
No major observations during the reporting month	-	-	-

6.2 Solid and Liquid Waste Management Status

The Contractor has been registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting was carried out on site. A sufficient number of receptacles were available for general refuse collection.

As advised by the Contractor, 1 tonne C&D material was generated on site during the period. 3 kg of metals was generated and collected by registered recycling collector. 2 kg of paper/cardboard packing and 2 kg of plastic were generated on site and collected by registered recycling collector. No chemical waste was generated and collected by licensed chemical waste collector. 8 kg of other types of wastes (e.g. general refuse) was generated on site and disposed of at public landfill facility.

The Contractor is advised to maintain on site waste sorting and recording system and maximize reuse / recycling of C&D wastes.

6.3 Status of Environmental Licenses and Permits

The environmental permits, licenses, and/or notifications on environmental protection for this Project which were valid during the reporting period is summarised in Table 6.2.

Table 6.2: Status of Environmental Submissions, Licenses and Permits

Statutory Reference	Description	Permit/Reference No.	Status
EIAO	Environmental Permit	EP-311/2008/D	Valid
APCO	Notification of Construction Work under APCO	316688 (27 Apr 2010)	Valid
WPCO	Discharge License	WT00007442-2010 (2 Nov 2010)	Valid
WDO	Registration as Chemical Waste Producer	WPN0000-542-H3083-04	Valid
WDO	Bill Account for disposal	700945423	Valid

Legend: EIAO – Environmental Impact Assessment Ordinance
APCO – Air Pollution Control Ordinance

WPCO – Water Pollution Control Ordinance
WDO – Waste Disposal Ordinance

6.4 Recommended Mitigation Measures

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental mitigation measures are provided in **Appendix L**. In particular, the following mitigation measures were brought to attention during the site audits:

Air Quality

- All stockpiles should be covered by tarpaulin or kept wet by water spraying;
- All vehicles should be washed to remove any dusty materials before leaving the construction sites;
- The portion of road leading the construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;
- During the dry season, sufficient water spraying should be provided at haul road to reduce dust emission; and
- Ensure proper functioning of the wheel wash facility.

Noise

- Mobile plant should be sited as far away from NSRs as possible;
- Plant known to emit noise strongly in one direction should be orientated to direct noise away from the NSRs; and
- The construction activities should be better scheduled to reduce noise nuisance.

Water Quality

- Effluent should be discharged in accordance with the discharge licence conditions;
- Soil contaminated with chemicals/oils should be removed from site and the voids should be created filled with suitable materials; and
- Silt and debris should be removed from the temporary drainage channel regularly.

Waste Management

- Reuse the excavated materials as far as practical to reduce the amount of waste disposal;
- C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal;
- Ensure drip trays are provided for chemical containers to prevent leakage or soil contamination;
- All plants and vehicles should be properly maintained to prevent oil leakage; and
- Oil stains on soil should be cleared by disposal of contaminated soil.

7 Report on Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions

7.1 Record on Non-compliance of Action and Limit Levels

There is no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting month.

During February 2014, some Action/Limit Level exceedances were observed at MP3 while no exceedance was observed at MP4, MP5 and MP6. A summary is presented in **Table 7.1** below.

Table 7.1: Summary of Exceedances in Water Quality

Monitoring Date	pH	Dissolved Oxygen (mg/L)	Turbidity (NT)	Suspended Solids (mg/L)
MP3				
04/02/2014	7.4	**5.1**	30.8	16
06/02/2014	7.5	**6.2**	38.3	14
08/02/2014	**7.6**	**5.8**	39.3	11
10/02/2014	7.5	9.5	23.1	16
12/02/2014	7.5	10.3	26.3	14
14/02/2014	7.5	9.3	27.6	6
17/02/2014	7.5	7.8	15.6	7
19/02/2014	7.5	9.5	20.5	10.5
21/02/2014	7.5	8.7	28.2	23
24/02/2014	7.4	7.9	17.9	25
26/02/2014	7.4	7.4	30.7	22.5
28/02/2014	7.4	8.4	**80.3**	**88**
Action Level	<5.5 or >7.5	<6.85	>64	>65
Limit Level	<4.0 or >8.0	<6.65	>67	>66
MP4				
04/02/2014	7.5	6.0	44.9	41.5
06/02/2014	7.4	6.3	32.5	15.5
08/02/2014	7.5	6.0	33.7	11
10/02/2014	7.4	9.0	26.7	20.5
12/02/2014	7.4	10.6	26.9	10.5
14/02/2014	7.4	9.5	21.2	10
17/02/2014	7.4	8.2	17.8	4
19/02/2014	7.4	9.1	28.2	13
21/02/2014	7.4	8.3	22.3	16.5
24/02/2014	7.4	7.8	18.9	20.5
26/02/2014	7.4	7.2	27.2	21.5
28/02/2014	7.4	8.5	32.5	19
Action Level	<5.5 or >7.5	<3.91	>60	>50
Limit Level	<4.0 or >8.0	<3.82	>64	>53
MP5				

Monitoring Date	pH	Dissolved Oxygen (mg/L)	Turbidity (NT)	Suspended Solids (mg/L)
04/02/2014	7.5	6.3	49.0	32.5
06/02/2014	7.5	5.4	36.7	10
08/02/2014	7.4	6.1	36.4	10.5
10/02/2014	7.4	8.7	28.1	21
12/02/2014	7.4	9.6	26.6	11.5
14/02/2014	7.4	8.9	21.5	10
17/02/2014	7.4	7.9	18.3	4
19/02/2014	7.4	9.0	28.6	11.5
21/02/2014	7.4	8.4	23.1	13
24/02/2014	7.4	8.1	16.8	16
26/02/2014	7.4	7.5	30.1	22.5
28/02/2014	7.4	8.3	30.7	19
Action Level	<5.5 or >7.5	<4.13	>81	>66
Limit Level	<4.0 or >8.0	<3.87	>84	>69
MP6				
04/02/2014	7.5	5.7	46.3	29
06/02/2014	7.5	5.4	32.3	12
08/02/2014	7.5	5.7	42.3	13.5
10/02/2014	7.4	8.3	27.3	15.5
12/02/2014	7.4	9.2	26.1	10.5
14/02/2014	7.4	9.7	22.6	10
17/02/2014	7.4	7.5	18.9	3.5
19/02/2014	7.4	8.4	28.2	13
21/02/2014	7.4	8.1	24.8	12
24/02/2014	7.4	7.2	16.2	17
26/02/2014	7.4	7.3	29.3	29.5
28/02/2014	7.4	7.8	29.6	19.5
Action Level	<5.5 or >7.5	<4.61	>94	>75
Limit Level	<4.0 or >8.0	<4.52	>96	>75

Notes:

(1) Values **Bold** indicate Action Level exceedance.

(2) Values **Underlined and Bold** indicate Limit Level exceedance.

7.2 Record on Environmental Complaints received

No new environmental complaint was received during the reporting month.

One environmental complaint received in January 2014 has been followed up and its description is reproduced below for the sake of convenience.

In January 2014, a formal complaint was made to the Environmental Protection Department (EPD) on dust impact at Palm Springs, Yuen Long. The complaint concerned suspected dust emissions from the Wo Shang Wai construction site. According to the complainant, the Contractor had not implemented suitable dust and mud prevention measures which had caused large air quality impact to Narcissus Path, Arcadia, Palm Springs, and area inside Palm Springs. The complainant further added that dust and mud nuisance over a long period from works in the Wo Shang Wai construction site had caused dust to settle in Narcissus Path and Banyan Path, Arcadia, Palm Springs. Mott MacDonald Hong Kong Limited as the Environmental Team (ET) for the Proposed Comprehensive Development at Wo Shang Wai, Yuen Long, received the formal complaint on 24 January 2014 via email from EPD. The findings of ET's investigation are presented in Section 7.4 below.

7.3 Record on Notifications of Summons and Successful Prosecution

No notifications of summons or successful prosecution were received the reporting month.

7.4 Review of Reasons for and Implications of Non-compliance, Complaints, Summons and Prosecutions

Non-compliance

Investigations have been carried out to identify the causes of water quality exceedance.

From investigation, construction activities during the period of exceedance included mainly site formation and foundation work, as well as pond drainage management in the Wetland Restoration Area (to lower the water level and remove unwanted species in the pond). It was observed that the Contractor has implemented water quality mitigation measures as recommended in the EIA report, including the provision of temporary drainage facility and associated treatment facility. Sand bags are in place in the temporary drainage channel to enhance the desilting efficiency. The Contractor further enhanced the water quality mitigation measures by erecting several segments of rock bunds and installing a barrier at the discharge outlet to desilt and divert site runoff to sedimentation tanks and wastewater treatment facilities (Aquased), which will ensure all site runoff is treated to satisfactory quality before discharging into the northern ditches. With external factors affecting the adjacent environments, such as natural variations, pond fish culture activities and rainfall, the exceedances were considered not due to Project construction works.

Complaints

From ET's investigation into the complaint, the major site activities conducted during January 2014 were consolidation of site formation and excavation/removal of C&D material. Potential dust sources from the site include dust from haul road and stockpiles, excavation/ loading of fill, backfilling, consolidation of site formation and movement of site vehicles, machineries and backfilling material.

Based on the site daily record provided by Contractor, the Contractor implemented the following air quality mitigation measures as recommended in EM&A Manual which include:

- Maintain and operate the automatic sprinkler system to ensure water spraying within the site boundary for dust suppression;
- Water spraying within the site boundary (by machineries and manpower) for dust suppression where the automatic sprinkler system cannot cover;
- Operation of water trucks for spraying of haul roads within the site boundary especially near the site boundary with Palm Springs / Royal Palms;
- Compaction of fill materials by rollers/excavators;
- Every load of dusty materials carried by vehicle was covered entirely to ensure that the dusty materials do not leak from the vehicle; and
- Every vehicle was washed to remove any dusty materials from its body and wheels before leaving the construction site.

Other potential dust sources that can be identified nearby include:
- Cement mixing and dust generating works from adjacent construction site;
- Construction of village houses nearby; and
- Traffic from San Tin Highway.

Regular weekly environmental site audits were conducted since the start of the EM&A programme in May 2010. During the site audit conducted jointly by ET, Independent Environmental Checker (IEC) and Contractor on 28 January 2014, regular wetting of the site area and haul roads by site staff and water truck near the site boundary with Palm Springs were observed. Furthermore, dump trucks were properly washed at the wheel wash pit prior to leaving the site.

During the site audits conducted by ET and Contractor on 11 and 18 February 2014, regular wetting of the site area and haul roads by water truck and compaction of fill materials by excavator were observed respectively.

Furthermore, during construction works within the Project site on 24 February 2014 regular wetting by automatic water sprinkler of the haul road near the site boundary with Palm Springs and by site staff of the excavation area near the site boundary with Palm Springs, as well as full covering of dump trucks during transport of C&D materials, were observed.

Dust monitoring was conducted since commencement of construction of the Project. No exceedance of action and limit levels for 24-hour Total Suspended Particulates (TSP) was recorded during December 2013 and January 2014. The maximum 24-hour TSP levels recorded at the four air quality monitoring stations AM1, AM2, AM3 and AM4 during this period were 112 $\mu g/m^3$, 124 $\mu g/m^3$, 115 $\mu g/m^3$ and 119 $\mu g/m^3$ respectively, which were well below the action levels of 226 $\mu g/m^3$, 213 $\mu g/m^3$, 205 $\mu g/m^3$ and 237 $\mu g/m^3$ respectively. Overall, no exceedance of action and limit levels for 24-hour Total Suspended Particulates (TSP) was recorded since commencement of construction of the Project.

No exceedance of action and limit levels for 1-hour TSP was recorded during December 2013 and January 2014. The maximum 1-hour TSP levels recorded at the four air quality monitoring stations AM1, AM2, AM3 and AM4 during this period were 264 $\mu g/m^3$, 256 $\mu g/m^3$, 262 $\mu g/m^3$ and 284 $\mu g/m^3$ respectively, which were below the action levels of 378 $\mu g/m^3$, 357 $\mu g/m^3$, 358 $\mu g/m^3$ and 372 $\mu g/m^3$ respectively. Overall,

exceedance of action levels for 1-hour TSP was recorded on 7 December 2010 only, however following investigation by ET it was concluded that the exceedances recorded were considered not due to construction works.

On the other hand, the prevailing wind direction in December 2013 and January 2014 was mostly northeast from the information obtained from the Hong Kong Observatory.

There was no deterioration of air quality observed durng the abovementioned site audits on 28 January, 11 February and 18 February 2014.

Summons and Prosecutions

Not applicable for this reporting month.

7.5 Follow-up Actions Taken

Non-compliance

As non-compliances have been recorded, the Event and Action Plan has been followed. Although it is considered that the exceedances were not related to the Project, the Contractor was reminded to implement the water quality mitigation measures in accordance with the recommendation stated in Section 5.6.1 – 5.6.4 of the EIA Report as far as practicable and regular spot check would be conducted on the nearby discharge by Contractor and inform ET for investigation.

To cater for the site runoff in wet season, the Contractor has further enhanced the water quality mitigation measures by erecting several segments of rock bunds and installing a barrier at the discharge outlet to desilt and divert site runoff to sedimentation tanks and wastewater treatment facilities (Aquased), which will ensure all site runoff is treated to satisfactory quality before discharging into the northern ditches.

Complaints

Air quality mitigation measures as recommended in the Implementation Schedule of the EM&A Manual have been implemented by Contractor to minimise the air quality nuisance arising from the site activities. Nevertheless, such measures can be enhanced. The Contractor was recommended to continue water spraying to mitigate against dust emissions during ongoing excavation works and also to haul roads, unpaved areas and dusty operations especially during dry weather condition. Site briefing on a weekly basis on environmental mitigation measures to site staff should be conducted to increase site staff environmental awareness.

Summons and Prosecutions

Not applicable for this reporting month.

7.6 Cumulative Statistics for Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics for complaints, notifications of summons and successful prosecutions for the Project account for period starting from the date of commencement of construction (i.e. 12 May 2010) to the end of the reporting month and are summarized in the **Table 7.2** below.

Table 7.2: Statistics for Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of summons	Successful prosecutions
This reporting month (Feb 2014)	0	0	0
From 12 May 2010 to end of the reporting month (Feb 2014)	8	0	0

8 Future Key Issues

8.1 Site Preparatory Works and Construction Works for the Coming Month

The major site works to be commissioned in the coming month include:

- Site formation
- Foundation work
- Pond drainage management (to lower the water level and remove unwanted species in the pond)

8.2 Key Issues for the Coming Months

Key issues to be considered in the coming three months include:

- Generation of dust from activities on-site during dry weather conditions;
- Noise impact from operating equipment and machinery on-site;
- Generation and treatment of site surface runoffs and wastewater from activities on-site and during wet weather conditions;
- Sorting, recycling, storage and disposal of general refuse and construction waste from activities on-site; and
- Management of chemicals and avoidance of oil spillage on-site and to the drainage.

8.3 Monitoring Schedule for the Coming Month

The environmental site inspection and environmental monitoring will be continued in the coming month. Impact monitoring for air, noise, water quality, ecology and landscape and visual in accordance with the approved EM&A Manual has commenced since 12 May 2010. The tentative monitoring schedule for March 2014 is shown in the **Table 8.1**.

Table 8.1: Tentative Environmental Monitoring and Audit Schedule for March 2014

Tentative Environmental Monitoring and Audit Schedule for Mar 2014

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1 **Landscape**
2	3 Water	4 **Bird** *	5 Water 24-hr TSP 1-hr TSP Noise Monitoring	6	7 Water	8
9	10 Water	11 **Bird** 24-hr TSP 1-hr TSP Noise Monitoring *	12 Water	13	14 Water **Landscape** @	15
16	17 Water 24-hr TSP 1-hr TSP Noise Monitoring	18 **Bird** **Dragonfly & Butterfly** **Water Quality (Ecology)** *	19 Water	20	21 Water 24-hr TSP 1-hr TSP	22
23	24 Water	25 **Bird** *	26 Water	27 24-hr TSP 1-hr TSP Noise Monitoring	28 Water **Landscape**	29
30	31 Water					

* Site Audit by Mott MacDonald (MM)

@ Report Submission (Monthly EM&A Report)

Ecological Surveys & Landscape Audits indicated in **bold font**

8.4 Conclusions and Recommendations

8.4.1 Conclusions

The EM&A programme as recommended in the EM&A manual has been undertaken in the reporting month since 12 May 2010.

Monitoring of Air Quality, Noise, Water Quality, Ecology and Landscape and Visual impacts due to the Project was under way. In particular, the 1-hr TSP, 24-hr TSP, noise level (as L_{eq}) and water quality parameters (such as pH, DO, turbidity and SS) under monitoring have been checked against established Action and Limit levels.

There was no breach of Action and Limit Levels for 1-hr TSP, 24-hr TSP and noise in the reporting month.

During February 2014, some Action/Limit Level exceedances were observed at MP3 while no exceedance was observed at MP4, MP5 and MP6.

One environmental complaint received in January 2014 has been followed up by ET. From ET's investigation conducted into the complaint, air quality mitigation measures as recommended in the Implementation Schedule of the EM&A Manual have been implemented by Contractor to minimise the air quality nuisance arising from the site activities. Nevertheless, such measures can be enhanced and recommendations were provided to the Contractor to further enhance the dust suppression within the site.

8.4.2 Recommendations

With considerations on the construction activities and environment, the following recommendations were provided:

Air Quality

- All stockpiles should be covered by tarpaulin or kept wet by water spraying;
- All vehicles should be washed to remove any dusty materials before leaving the construction sites;
- The portion of road leading the construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;
- During the dry season, sufficient water spraying should be provided at haul road to reduce dust emission; and
- Ensure proper functioning of the wheel wash facility.

Noise

- Mobile plant should be sited as far away from NSRs as possible;
- Plant known to emit noise strongly in one direction should be orientated to direct noise away from the NSRs; and
- The construction activities should be better scheduled to reduce noise nuisance.

Water Quality

- Effluent should be discharged in accordance with the discharge licence conditions;
- Soil contaminated with chemicals/oils should be removed from site and the voids should be created filled with suitable materials; and
- Silt and debris should be removed from the temporary drainage channel regularly.

Waste Management

- Reuse the excavated materials as far as practical to reduce the amount of waste disposal;
- C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal;
- Ensure drip trays are provided for chemical containers to prevent leakage or soil contamination;
- All plants and vehicles should be properly maintained to prevent oil leakage; and
- Oil stains on soil should be cleared by disposal of contaminated soil.

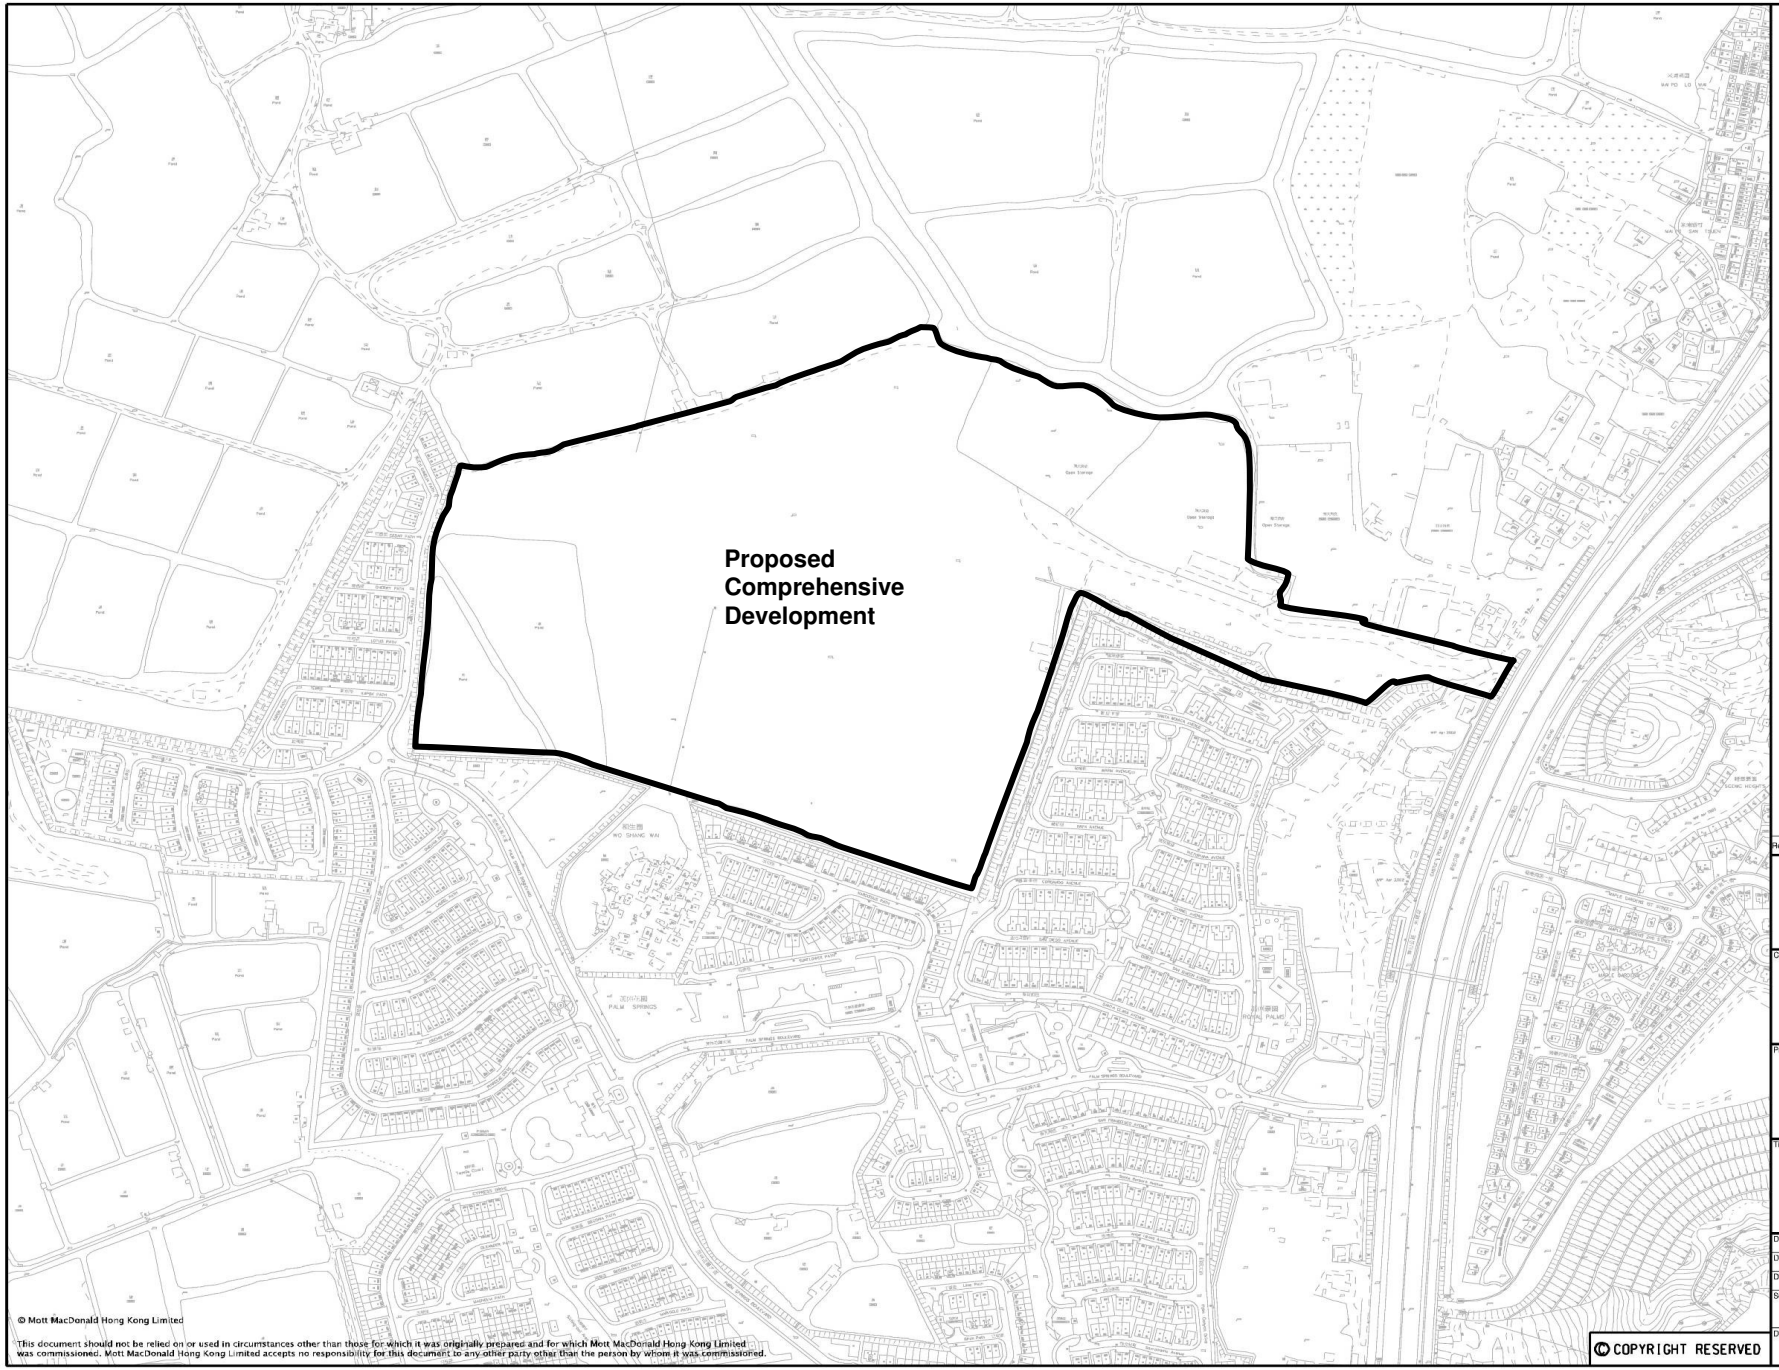

Legend:

Site Boundary

Rev	Date	Drawn	Description	Ch'k'd	App'd

Mott MacDonald

Mott MacDonald Hong Kong Ltd
7th Floor
West Wing Office Building
New World Centre
20 Salisbury Road
Tsim Sha Tsui, Kowloon
Hong Kong

Tel 2828 5757
Fax 2827 1823
Web www.mottmac.com.hk

Client

HENG SHUNG CONSTRUCTION CO. LTD

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

General Layout Plan of the Project Site

Designed			Eng.Chk.		
Drawn			Coordination		
Dwg.Chk.			Approved		
Scale		Project		Status	
		CAD File J:\22005\REPORT\ENV\EN&A_manual\080430\BaseMap.dgn			
Drawing No.				Rev	

Figure 1.1

© Mott MacDonald Hong Kong Limited

This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Hong Kong Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.

© COPYRIGHT RESERVED

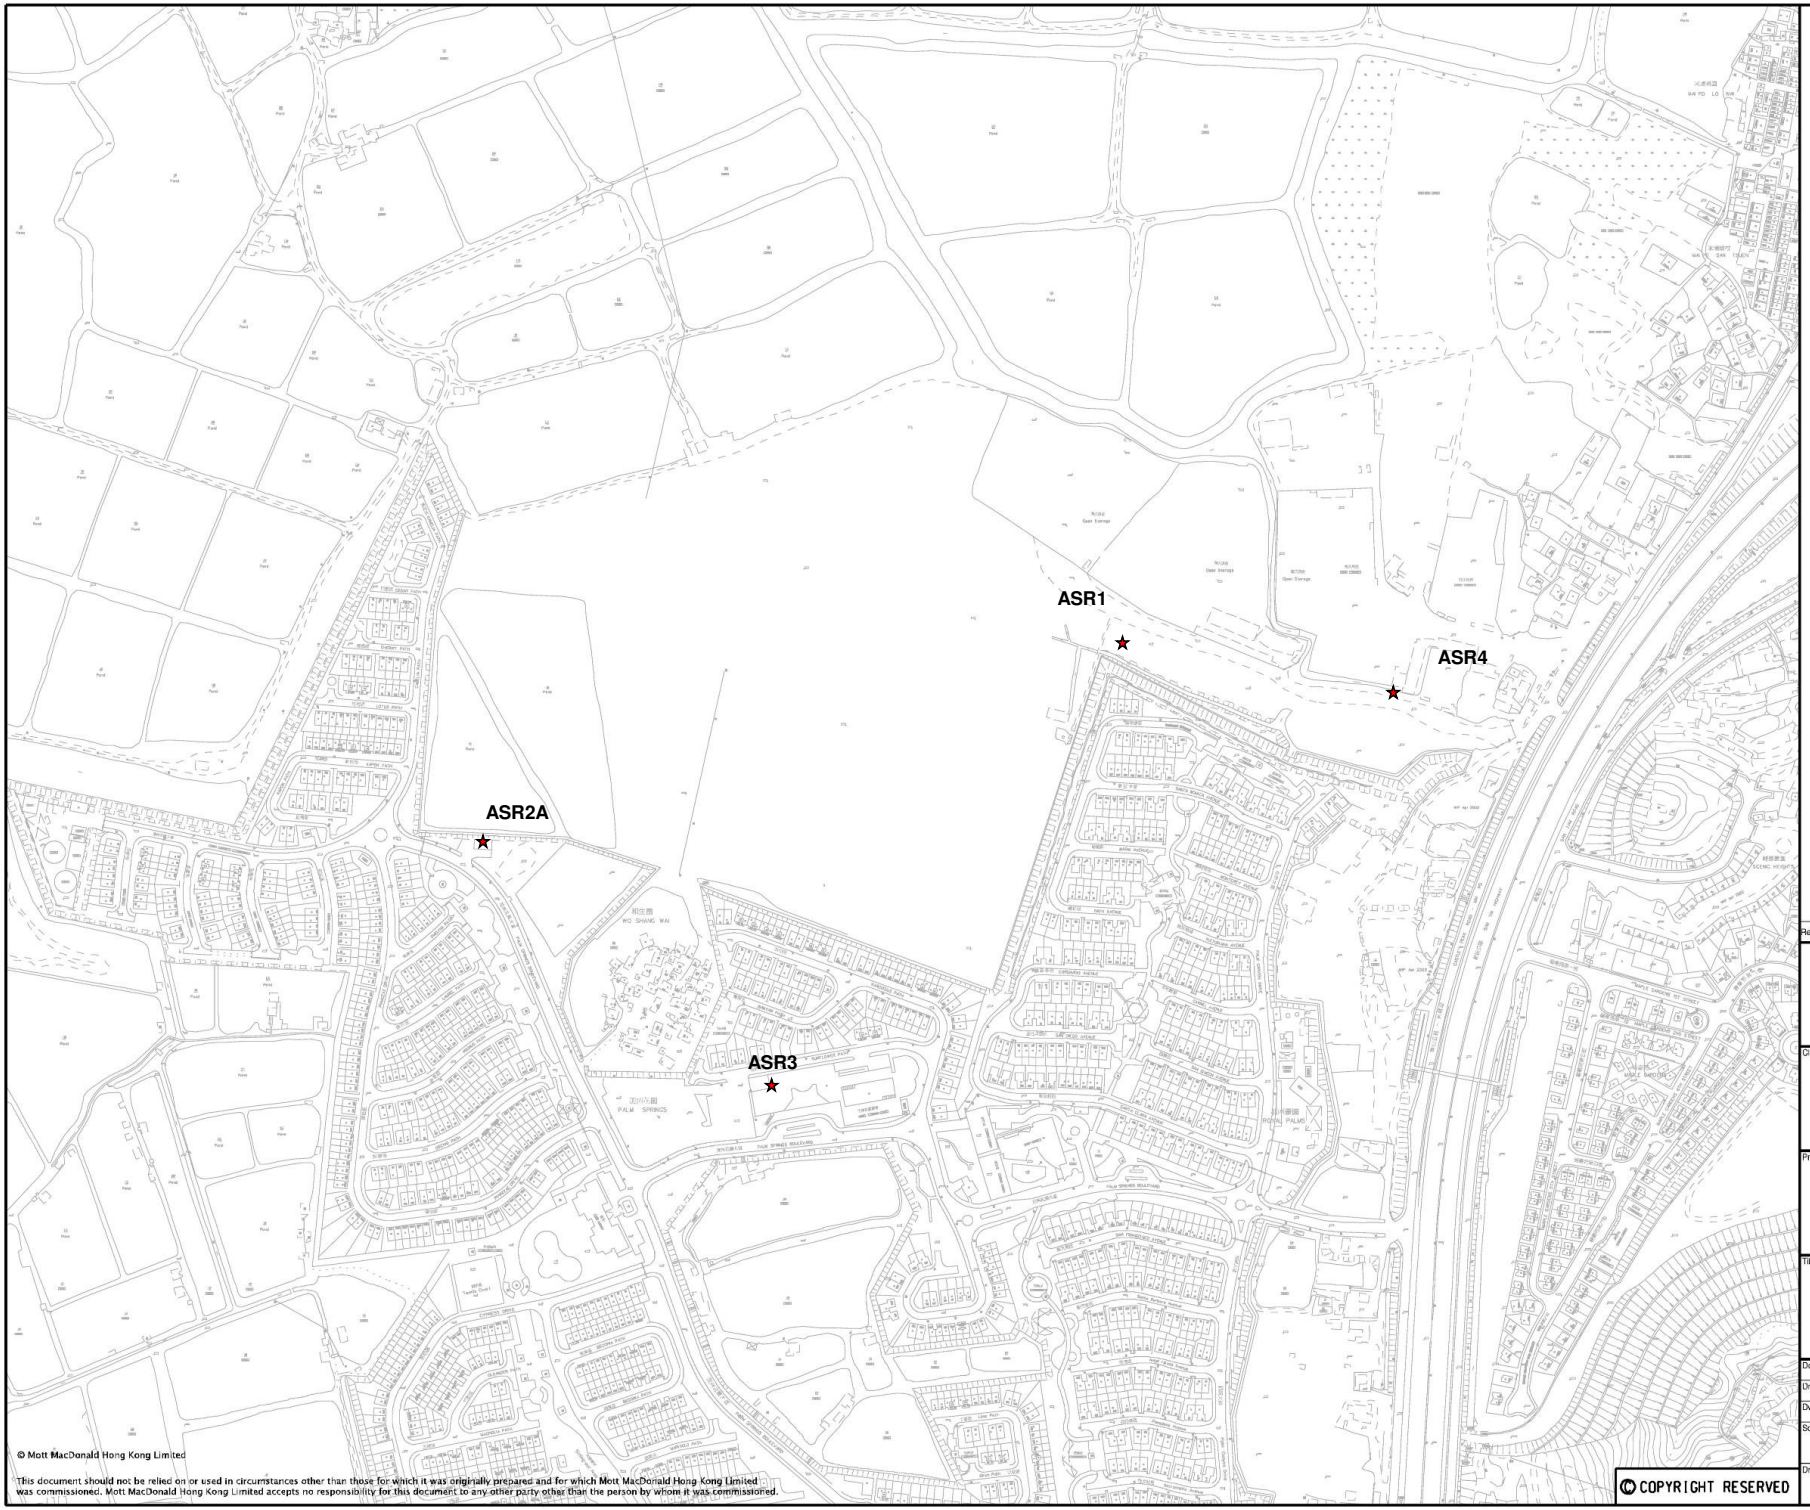

© Mott MacDonald Hong Kong Limited

This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Hong Kong Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.

© COPYRIGHT RESERVED

Legend:

★ Construction Phase Air Quality Monitoring Locations

Rev	Date	Drawn	Description	Ch'k'd	App'd

Mott MacDonald

Mott MacDonald Hong Kong Ltd
20/F, AIA Kowloon Tower
Landmark East
100 How Ming Street
Kwun Tong, Kowloon
Hong Kong
Tel 2828 5757
Fax 2827 1823
Web www.mottmac.com.hk

Client

HENG SHUNG CONSTRUCTION CO. LTD

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

Locations of Air Quality Monitoring Stations

Designed			Eng.Chk.		
Drawn			Coordination		
Dwg.Chk.			Approved		
Scale		Project		Status	
		CAD File J:\22005\REPORT\ENV\EM&A_manual\060301\BaseMap.dgn			

Drawing No. Figure 2.1 Rev

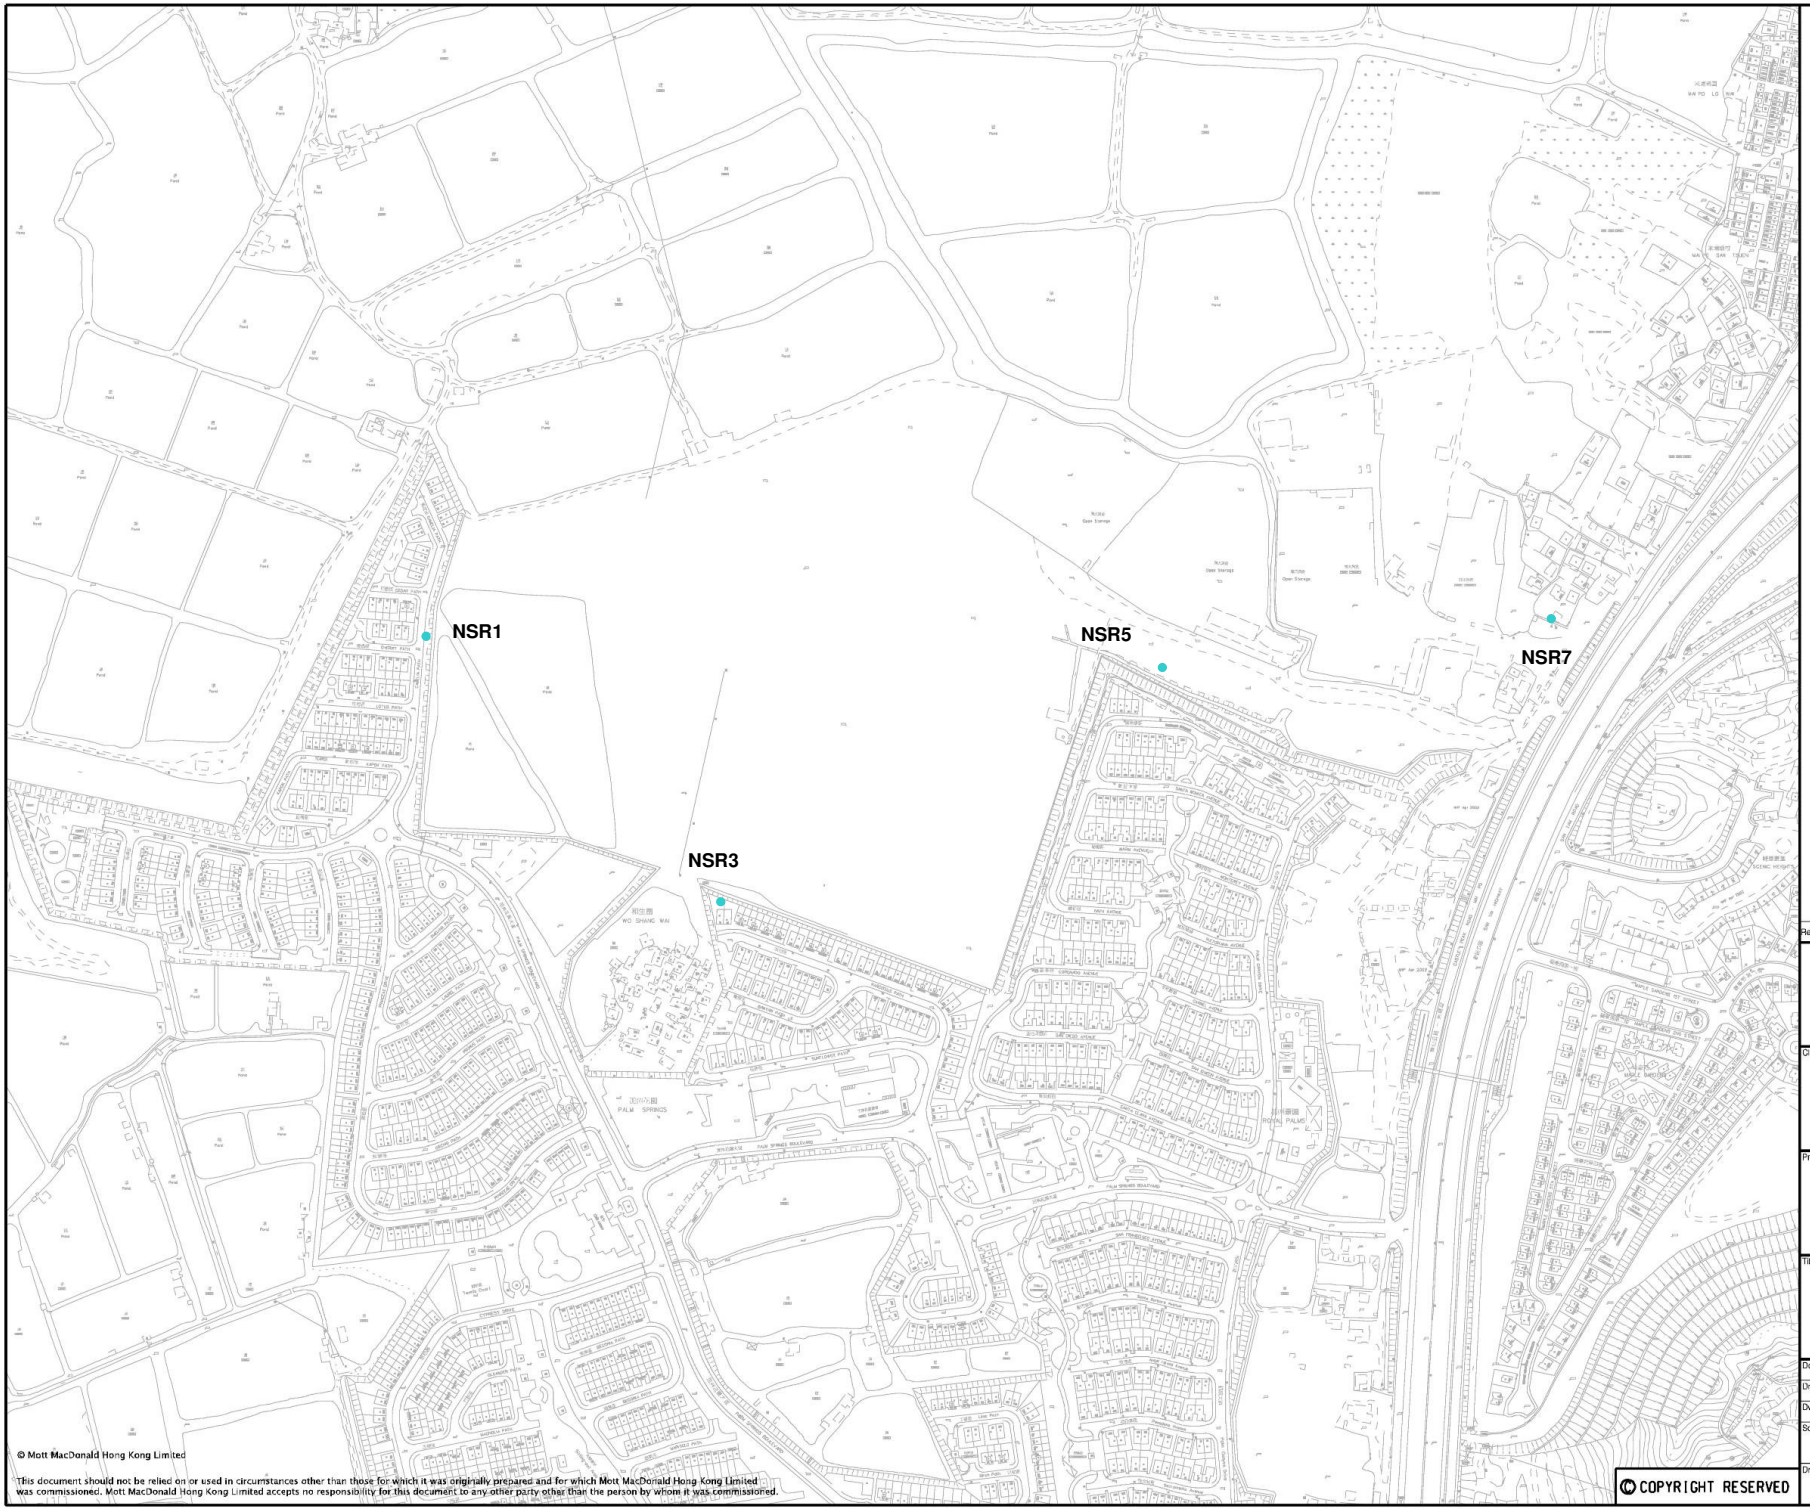

© Mott MacDonald Hong Kong Limited

This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Hong Kong Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.

© COPYRIGHT RESERVED

Legend:

- Construction Phase Noise Monitoring Stations

Rev	Date	Drawn	Description	Ch'k'd	App'd

Mott MacDonald

Mott MacDonald Hong Kong Ltd
20/F, AIA Kowloon Tower
Landmark East
100 How Ming Street
Kwun Tong, Kowloon
Hong Kong
Tel 2828 5757
Fax 2827 1823
Web www.mottmac.com.hk

Client

HENG SHUNG CONSTRUCTION CO. LTD

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

Locations of Noise Monitoring Stations

Designed			Eng.Chk.		
Drawn			Coordination		
Dwg.Chk.			Approved		
Scale		Project		Status	
		CAD File J:\221005\REPORT\ENV\EM&A_manual\060301\BaseMap.dgn			

Drawing No.

Figure 2.2

Rev

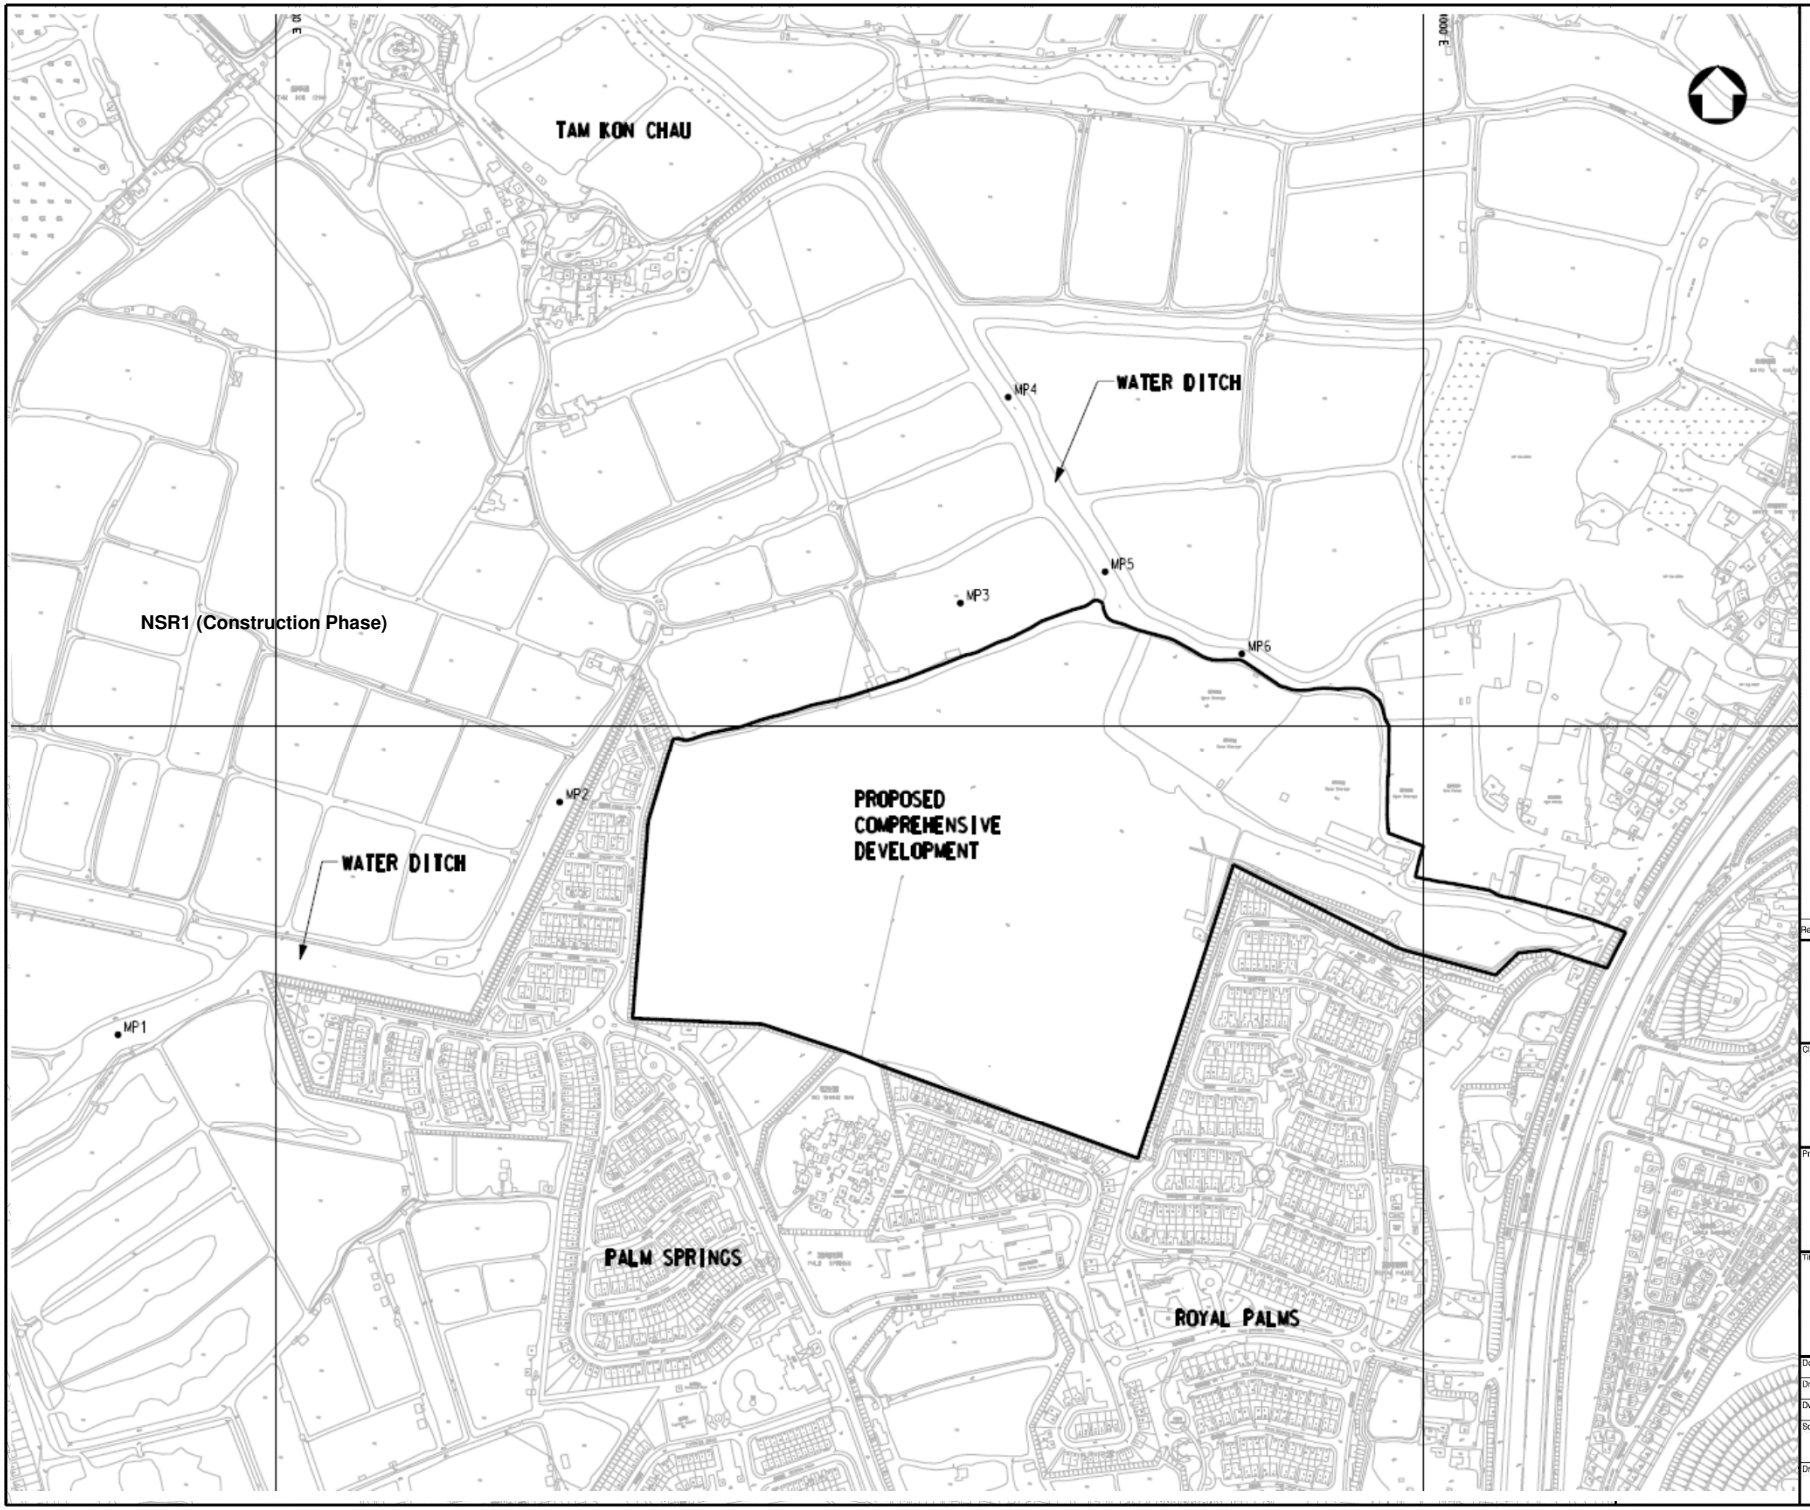

Legend:

- Water Quality Sampling Stations

Rev	Date	Drawn	Description	Ch'k'd	App'd

Mott MacDonald

Mott MacDonald Hong Kong Ltd
20/F, AIA Kowloon Tower
Landmark East
100 How Ming Street
Kwun Tong, Kowloon
Hong Kong
Tel 2828 5757
Fax 2827 1823
Web www.mottmac.com.hk

Client

HENG SHUNG CONSTRUCTION CO. LTD

Project

PROPOSED COMPREHENSIVE DEVELOPMENT
AT WO SHANG WAI, YUEN LONG

Title

Locations of Water Quality Monitoring Stations

Designed			Eng.Chk.		
Drawn			Coordination		
Dwg.Chk.			Approved		
Scale		Project		Status	
		CAD File			

Drawing No. Figure 2.3 Rev

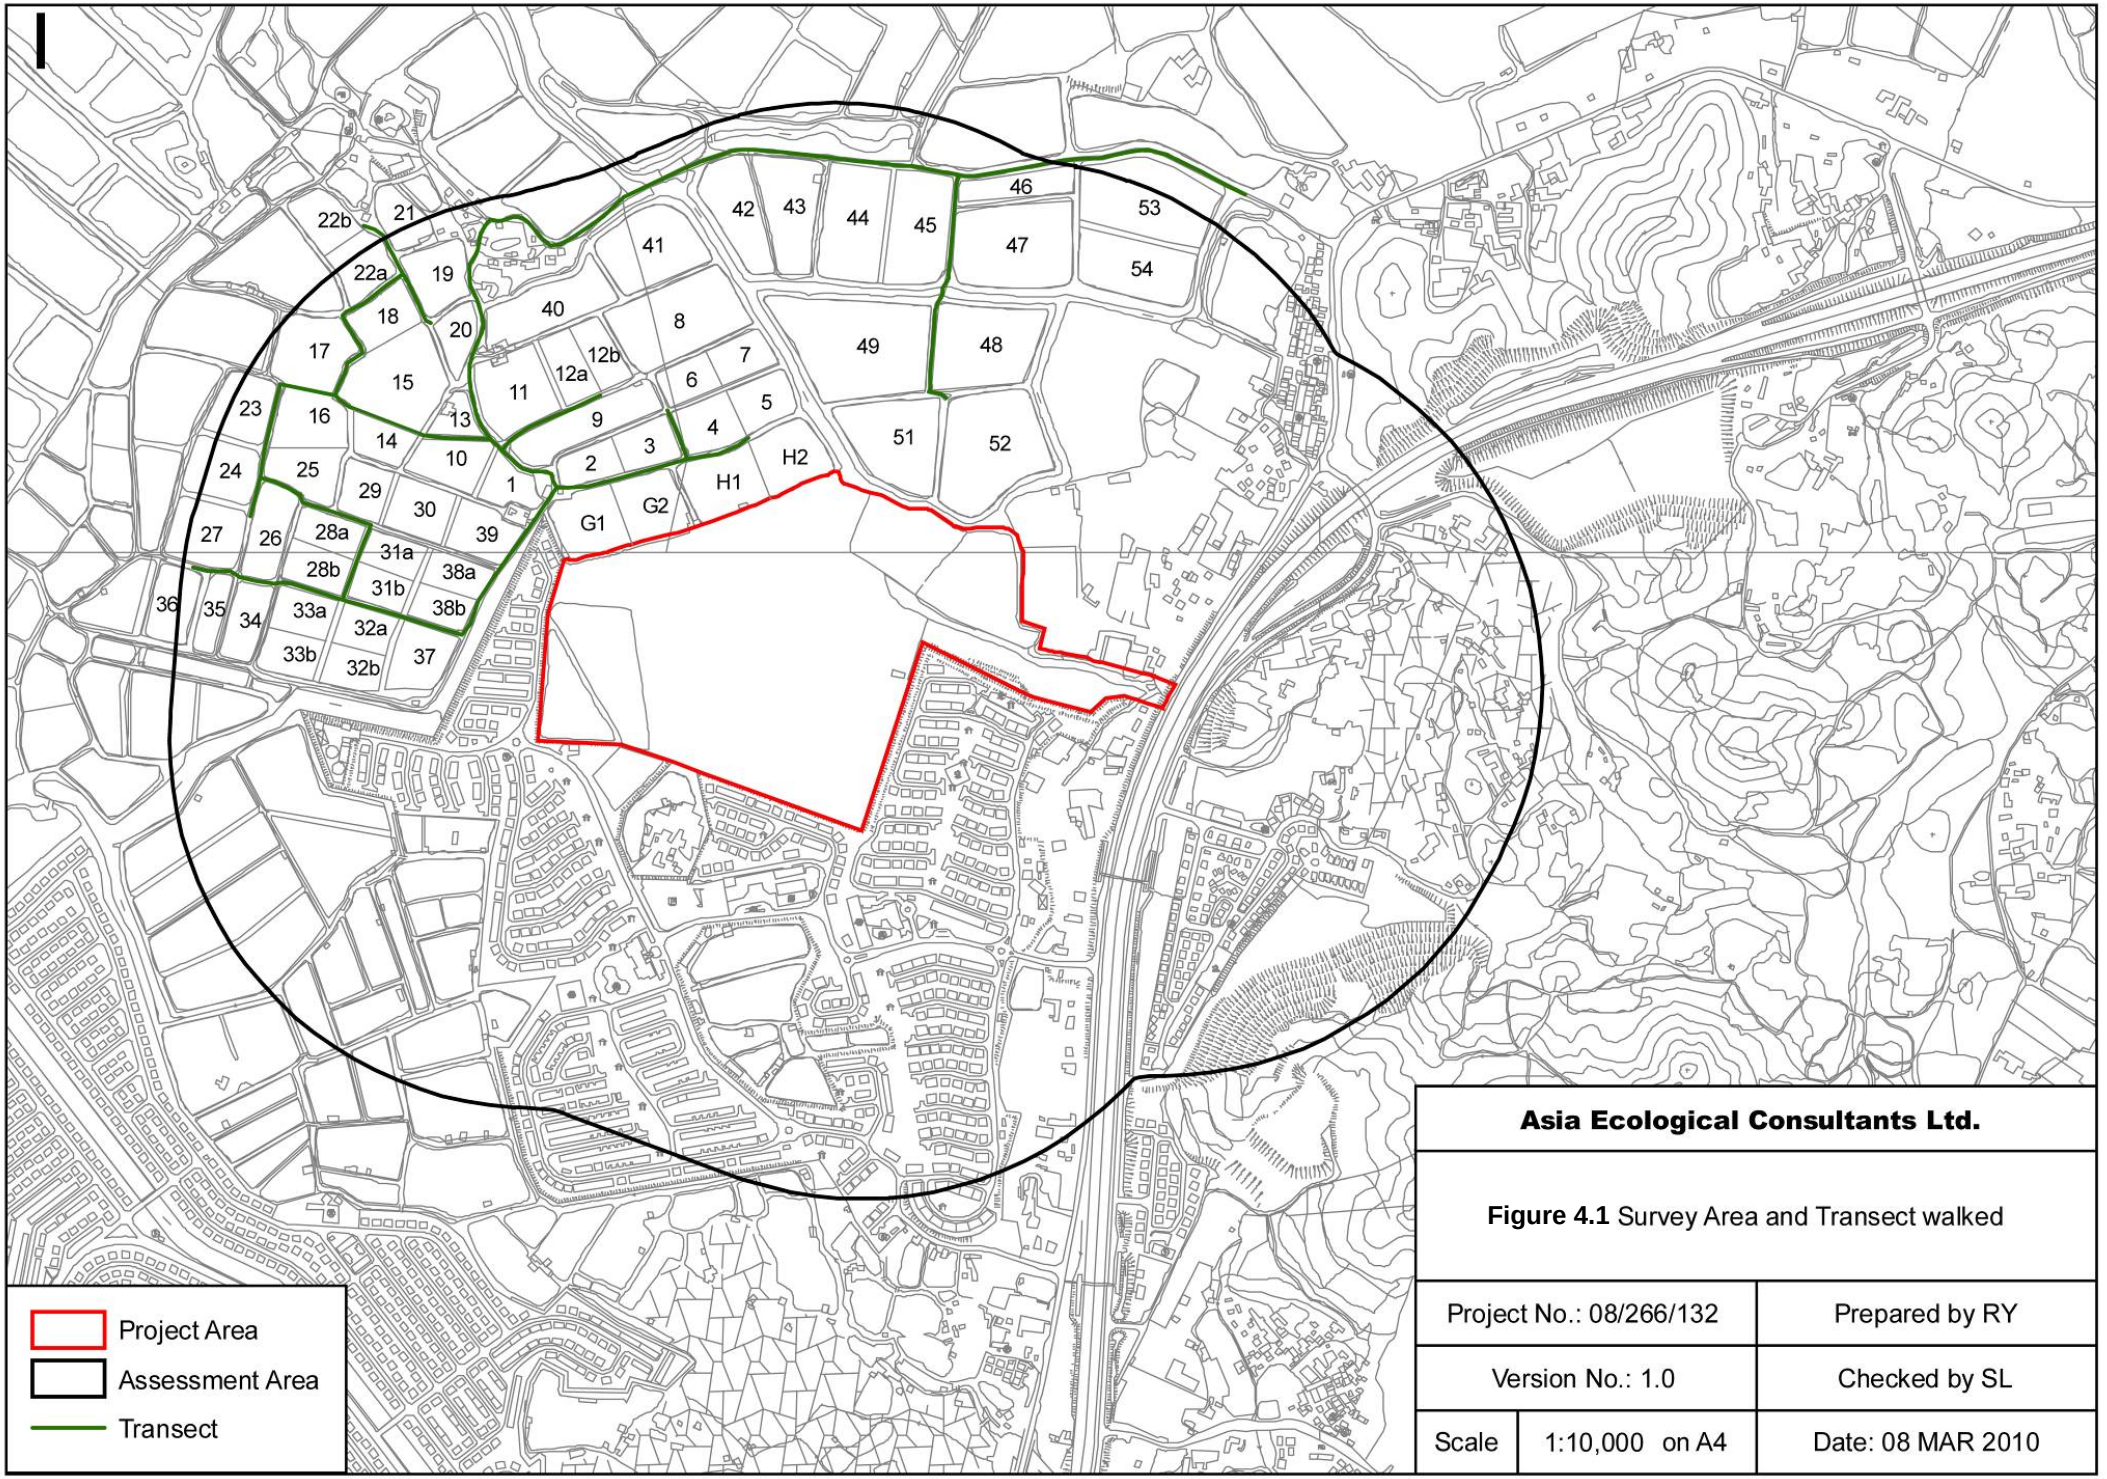

Asia Ecological Consultants Ltd.

Figure 4.1 Survey Area and Transect walked

Project No.: 08/266/132		Prepared by RY
Version No.: 1.0		Checked by SL
Scale	1:10,000 on A4	Date: 08 MAR 2010

Appendix A. Project Organization Chart

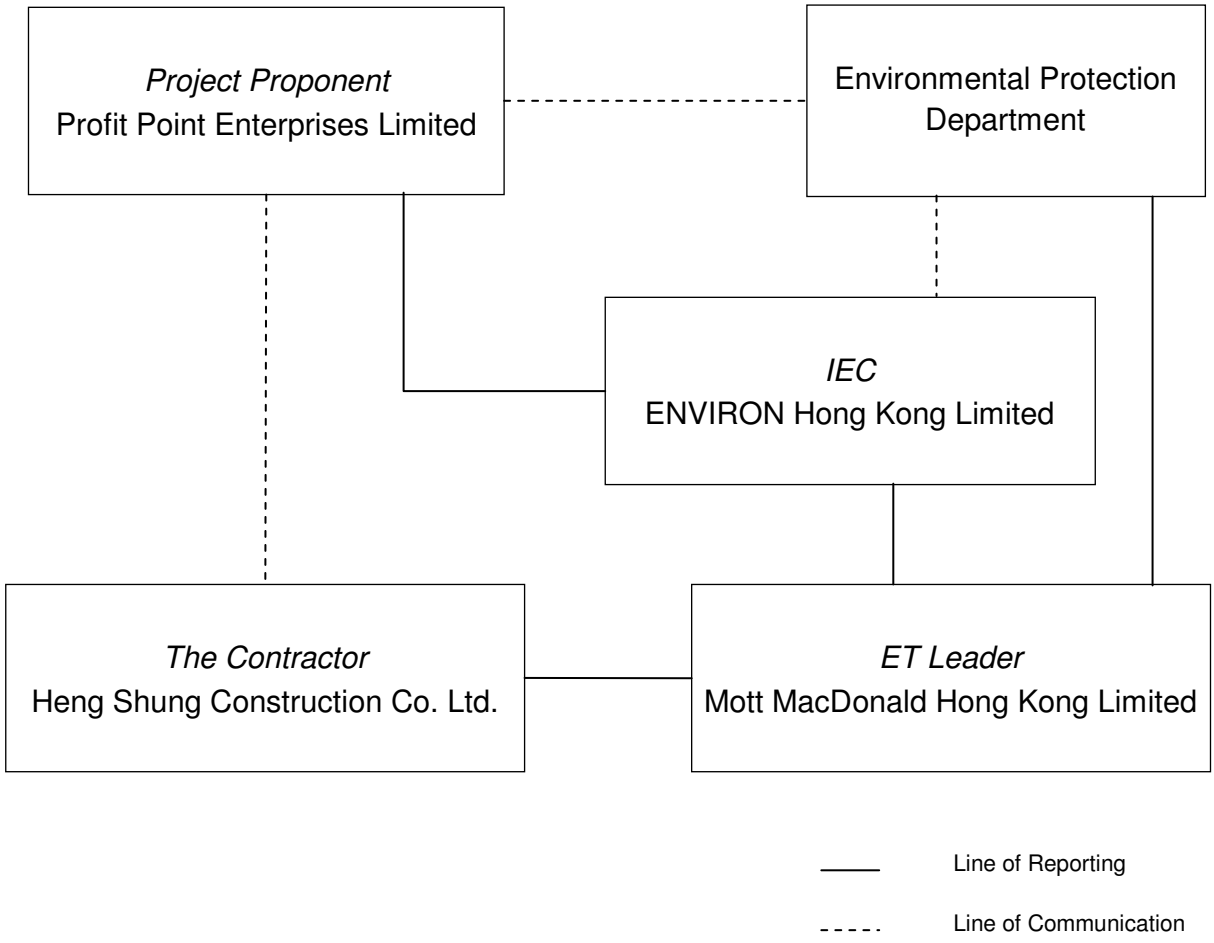

Contact information:

Company	Position	Name	Telephone
Profit Point Enterprises Limited (Project Proponent)	Project Manager	Mr. Kelvin LAU	2908 8114
Heng Shung Construction Co. Ltd. (The Contractor)	Assistant Construction Manager	Ms. Lynne HUNG	2908 2391
	Site Agent	Mr. MOK Wing Hong	9866 7683
	Environmental Officer	Mr. Ricky WONG	9866 7625
ENVIRON Hong Kong Ltd. (Independent Environmental Checker (IEC))	Independent Environmental Checker	Mr. David YEUNG	3743 0788
Mott MacDonald Hong Kong Ltd. (Environmental Team (ET))	Environmental Team Leader	Mr. Terence KONG	2828 5919

Appendix B. Tentative Construction Programme

Wo Shang Wai Construction Works Programme (Phase I) (except TOA)

ID	Task Name	Working	Start	Finish
0	**Wo Shang Wai Construction Phase**	**2209 days**	**Wed 13/01/10**	**Fri 31/03/17**
1	Noise Barrier	85 days	Wed 13/01/10	Sat 24/04/10
2	WRA Site Formation Works	168 days	Mon 26/04/10	Mon 15/11/10
3	Install Band Drain	456 days	Thu 17/06/10	Sat 31/12/11
4	Trial Embankment	600 days	Thu 17/06/10	Sat 30/06/12
5	Site Formation	1214 days	Mon 03/01/11	Wed 31/12/14
6	Foundation Work	392 days	Wed 01/10/14	Thu 31/12/15
7	Superstructure	418 days	Mon 02/03/15	Thu 30/06/16
8	Finishing	549 days	Wed 01/07/15	Fri 31/03/17

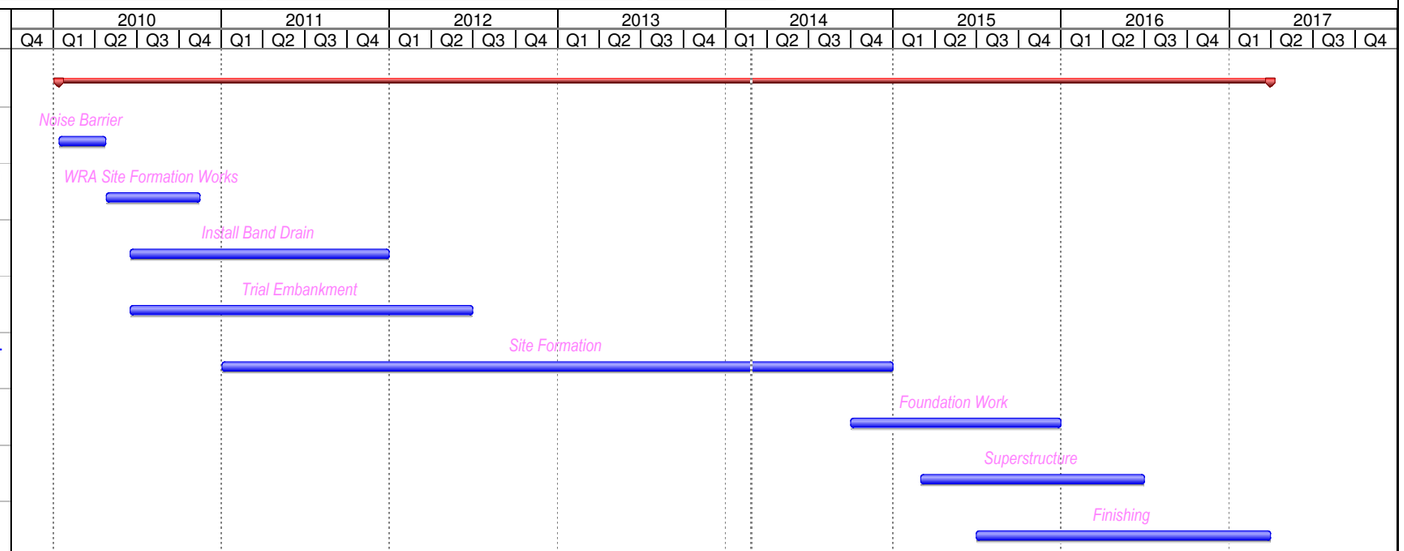

Project : Wo Shang Wai
Revision : I
Print Date : Tue 25/02/14

Task Milestone Summary

Appendix C. Action and Limit Levels for Construction Phase

Air Quality

Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level (µg/m^3)	Limit Level (µg/m^3)
ASR1	226	260
ASR2A	213	260
ASR3	205	260
ASR4	237	260

Action and Limit Levels for 1-hour TSP

Monitoring Station	Action Level (µg/m^3)	Limit Level (µg/m^3)
ASR1	378	500
ASR2A	357	500
ASR3	358	500
ASR4	372	500

Noise

Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
NSR1, NSR3, NSR5, NSR7		
0700 – 1900 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75 dB(A)

Water Quality

Action and Limit Levels for Water Quality

Parameters	DO in mg/L		Turbidity in NTU		SS in mg/L		pH	
	Action Level	Limit Level	Action Level	Action Level	Action Level	Limit Level	Action Level	Limit Level
MP1	1.23	1.17	173	177	231	299	< 5.5 or > 7.5	< 4.0 or > 8.0
MP2	1.04	0.89	132	163	170	209		
MP3	6.85	6.65	64	67	65	66		
MP4	3.91	3.82	60	64	50	53		
MP5	4.13	3.87	81	84	66	69		
MP6	4.61	4.52	94	96	75	75		

Appendix D. Event and Action Plan for Air Quality, Noise, Water Quality, Ecology and Landscape & Visual

Air Quality

Event	Action ET Leader	IEC	ER	Contractor
Action Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures. 2. Inform IEC and ER. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET. 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice. 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify the source. 2. Inform IEC and ER. 3. Advise ER on the effectiveness of the proposed remedial measures 4. Repeat measurements to confirm findings. 5. Increase monitoring frequency to daily. 6. Discuss with IEC and the Contractor on remedial actions required. 7. If exceedance continues, arrange meeting with IEC and ER. 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET. 2. Check the Contractor's working method. 3. Discuss with ET Leader and the Contractor on possible remedial measures. 4. Advise ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial actions to IEC within 3 working days of notification. 2. Implement the agreed proposals. 3. Amend proposal if appropriate.
Limit Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures. 2. Inform ER and EPD. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET. 2. Check the Contractor's working method. 3. Discuss with ET Leader and the Contractor on possible remedial measures. 4. Advise ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Amend proposal if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, EPD and the Contractor. 2. Identify the source. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. 6. Arrange meeting IEC and ER to discuss the remedial actions to be taken. 7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary and advise ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. In consultation with IEC, agree with the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by ER until the exceedance is abated.

Construction Noise

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level	1. Notify IEC and the Contractor. 2. Carry out investigation. 3. Report the results of investigation to IEC and the Contractor. 4. Discuss with the Contractor and formulate remedial measures. 5. Increase monitoring frequency to check mitigation measures.	1. Review with analysed results submitted by ET. 2. Review the proposed remedial measures by the Contractor and advise ER accordingly. 3. Supervise the implement of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals to IEC. 2. Implement noise mitigation proposals.
Limit Level	1. Identify the source. 2. Notify IEC, ER, EPD and the Contractor. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency. 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented. 6. Inform IEC, ER, and EPD the causes & actions taken for the exceedances. 7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the ER until the exceedance is abated.

Water Quality

Event	Action ET Leader	IEC	ER	Contractor
Action Level				
1. Exceedance for one sample	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; and 6. Repeat measurement on next day of exceedance.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; and 2. Make agreement on the mitigation measures to be implemented.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER; and 6. Implement the agreed mitigation measures.
2. Exceedance for two or more consecutive samples	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; and 8. Repeat measurement on next day of exceedance.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; and 6. Implement the agreed mitigation measures.
Limit Level				
1. Exceedance for one sample	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact;	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; and	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable

Event	Action			
	ET Leader	IEC	ER	Contractor
	3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; and 7. Increase the monitoring frequency to daily until no exceedance of Limit level.	submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; and 4. Assess the effectiveness of the implemented mitigation measures.	practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days; and 6. Implement the agreed mitigation measures.
2. Exceedance for two or more consecutive samples	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; and 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; and 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; and 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures; and 7. As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities.

Appendix E. Calibration Certificates

Appendix E
Calibration Record
(Air Quality Monitoring)

CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA
Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition		
Temperature	74.5 (23.6)	°F (°C)
Relative Humidity	51	%RH
Barometric Pressure	28.90 (978.7)	inHg (hPa)

Model	**AM510**
Serial Number	**11108010**

☒ As Left ☐ As Found

☒ In Tolerance ☐ Out of Tolerance

Concentration Linearity Plot

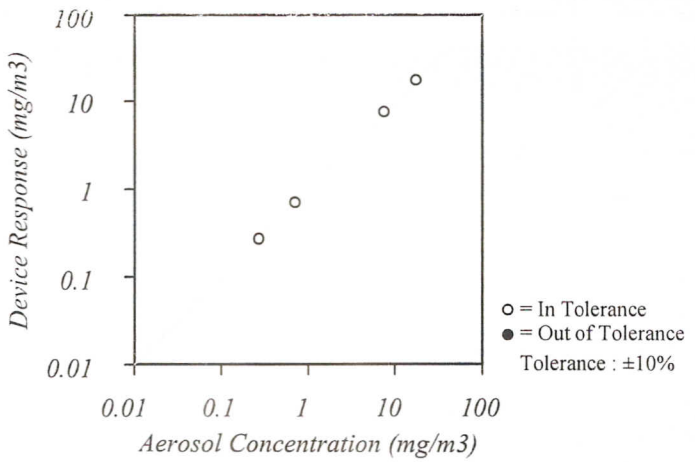

System ID: DTII01-02

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	03-12-13	03-12-14	Temperature	E002873	11-08-12	11-08-13
Humidity	E002873	11-08-12	11-08-13	DC Voltage	E003314	01-02-13	01-02-14
DC Voltage	E003315	01-02-13	01-02-14	Photometer	E003319	08-14-13	02-14-14
Microbalance	M001324	01-04-13	01-04-15	Pressure	E003511	11-07-12	11-07-13
Flowmeter	E002006	03-05-13	03-05-14				

Amanda Thad
Calibrated

☒ Final Function Check

August 21, 2013
Date

TSI P/N 2300157

CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA
Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition		
Temperature	67.6 (19.8)	°F (°C)
Relative Humidity	57	%RH
Barometric Pressure	28.69 (971.6)	inHg (hPa)

Model	**8520**
Serial Number	**85202623**

☒ As Left ☐ As Found

☒ In Tolerance ☐ Out of Tolerance

Concentration Linearity Plot

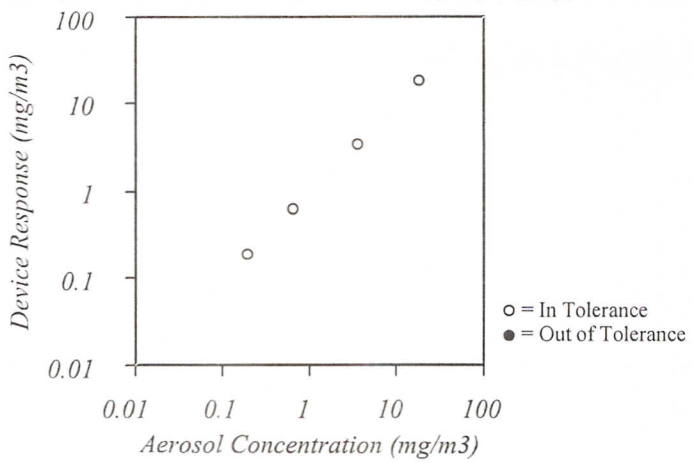

System ID: DTII01-02

Zero Stability Results			
Average: 0.000 :mg/m³	Minimum: 0.000 :mg/m³	Maximum: 0.001 :mg/m³	Time: 2.00 :hrs.

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	03-12-13	03-12-14
Humidity	E002873	11-08-12	11-08-13
DC Voltage	E003315	01-02-13	01-02-14
Microbalance	M001324	01-04-13	01-04-15
Flowmeter	E002006	03-05-13	03-05-14

Measurement Variable	System ID	Last Cal.	Cal. Due
Temperature	E002873	11-08-12	11-08-13
DC Voltage	E003314	01-02-13	01-02-14
Photometer	E003319	02-19-13	08-19-13
Pressure	E003511	11-07-12	11-07-13

Calibrated

☑ Final Function Check

July 23, 2013
Date

TSI P/N 2300157

High-Volume TSP Sampler
5-Point Calibration Record

Location : ASR2A
Calibrated by : P.F.Yeung
Date : 05/01/2014

Sampler
Model : GMWS-2310 ACCU-VOL
Serial Number : S/N 1061

Calibration Orfice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 12 Mar 2013
Slope (m) : 2.05818
Intercept (b) : 0.01929
Correlation Coefficient(r) : 0.99991

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1022
Ta(K) : 289

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	10.6	3.321	1.604	52	53.0
2	13 holes	9.0	3.060	1.477	46	46.9
3	10 holes	6.7	2.640	1.273	39	39.8
4	7 holes	5.0	2.281	1.099	32	32.6
5	5 holes	3.1	1.796	0.863	22	22.4

Sampler Calibration Relationship

Slope(m):40.546 Intercept(b):-12.261 Correlation Coefficient(r): 0.9991

Checked by: Magnum Fan Date: 10/01/2014

High-Volume TSP Sampler
5-Point Calibration Record

Location : ASR4
Calibrated by : P.F.Yeung
Date : 05/01/2014

Sampler
Model : GMWS-2310 ACCU-VOL
Serial Number : S/N 1273

Calibration Orfice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 12 Mar 2013
Slope (m) : 2.05818
Intercept (b) : 0.01929
Correlation Coefficient(r) : 0.99991

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1022
Ta(K) : 289

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	11.0	3.383	1.634	54	55.08
2	13 holes	9.1	3.077	1.486	47	47.94
3	10 holes	6.6	2.620	1.264	39	39.78
4	7 holes	4.8	2.235	1.076	32	32.64
5	5 holes	2.8	1.707	0.820	22	22.44

Sampler Calibration Relationship

Slope(m):39.457 Intercept(b):-9.981 Correlation Coefficient(r): 0.9993

Checked by: Magnum Fan Date: 10/01/2014

High-Volume TSP Sampler
5-Point Calibration Record

Location : ASR3
Calibrated by : K.T.Ho
Date : 05/01/2014

Sampler
Model : GMWS-2310 ACCU-VOL
Serial Number : S/N 7577

Calibration Orfice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 12 Mar 2013
Slope (m) : 2.05818
Intercept (b) : 0.01929
Correlation Coefficient(r) : 0.99991

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1022
Ta(K) : 289

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	12.0	3.533	1.707	58	59.16
2	13 holes	9.5	3.144	1.518	50	50.99
3	10 holes	6.8	2.660	1.283	41	41.82
4	7 holes	4.6	2.188	1.053	32	32.64
5	5 holes	3.1	1.796	0.863	23	23.46

Sampler Calibration Relationship

Slope(m):41.644 Intercept(b): -11.898 Correlation Coefficient(r): 0.9994

Checked by: Magnum Fan Date: 10/01/2014

High-Volume TSP Sampler
5-Point Calibration Record

Location	:	ASR1
Calibrated by	:	P.F.Yeung
Date	:	05/0/2014

Sampler

Model	:	GMWS-2310 ACCU-VOL
Serial Number	:	S/N 1806

Calibration Orfice and Standard Calibration Relationship

Serial Number	:	2454
Service Date	:	12 Mar 2013
Slope (m)	:	2.05818
Intercept (b)	:	0.01929
Correlation Coefficient(r)	:	0.99991

Standard Condition

Pstd (hpa)	:	1013
Tstd (K)	:	298.18

Calibration Condition

Pa (hpa)	:	1022
Ta(K)	:	289

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	11.4	3.444	1.664	55	56.10
2	13 holes	8.8	3.026	1.461	48	48.96
3	10 holes	7.2	2.737	1.320	42	42.84
4	7 holes	5.0	2.281	1.099	34	34.68
5	5 holes	2.7	1.676	0.805	24	24.48

Sampler Calibration Relationship

Slope(m):37.128 Intercept(b):-5.732 Correlation Coefficient(r): 0.9994

Checked by: Magnum Fan Date: 10/01/2014

Appendix E
Calibration Record
(Noise Monitoring)

TEST REPORT
for
PRECISION
SOUND LEVEL METER
(NX-42EX installed)

Model : NL－52

Serial No. : 00131627

Microphone No. : 04663

Preamplifier No. : 21571

Condition : Temperature 25 ℃

Humidity 33 %RH

Date : February, 26, 2013

Signature :

RION CO., LTD.

1. Frequency weightings (Fig. 1) Pass

Frequency weighting A

Frequency weighting C

Frequency weighting Z

2. Level linearity error (dB)

Reference signal level (Ref.) : 94.0 dB (at 1 kHz, 8 kHz), 74.0 dB (at 31.5 Hz)

Frequency weighting : A

Frequency \ Indicated value	Difference with Reference signal level (dB)						
	25.0	74.0	94.0	98.0	114.0	136.0	138.0
31.5 Hz	−0.2	Ref.	—	−0.1	—	—	—
1 kHz	−0.1	—	Ref.	—	0.0	—	−0.1
8 kHz	0.0	—	Ref.	—	—	0.0	—
Tolerance limit	±0.3	—	—	±0.3	±0.2	±0.3	±0.3

3. Toneburst response (Time weighted sound level)

Input signal level : 127 dB

Toneburst : Frequency : 4 kHz, duration : 0.25 ms

Frequency weighting : A, Time-weighting : F

(dB)			
Design goal	Indicated value	Difference	Tolerance limit
100.0	99.9	−0.1	±1.0

4. Time weighting I (impulse)

Input signal level : 120 dB

Toneburst : Frequency : 4 kHz, duration : 5 ms, period : 500 ms

Frequency weighting : A

(dB)			
Design goal	Indicated value	Difference	Tolerance limit
111.2	110.4	−0.8	±2.0

*When the optional Extended Function Program NX-42EX is installed, time weighting I(impulse) can be selected in only sub-channel.

5. Peak sound level (dB)

Frequency weighting : C

Frequency (Hz)	Number of cycles in test signal	(dB)				
		Input signal level	Design goal	Indicated value	Difference	Tolerance limit
			L_C	L_{Cpeak}		
31.5	1 cycle	137.0	136.5	137.3	0.8	±2.0
500	Positive half cycle	137.0	139.4	139.2	−0.2	±1.0
	Negative half cycle	137.0	139.4	139.2	−0.2	±1.0

6. Response to repeated to toneburst

Input signal level : 130.0 dB + 8 dB

Frequency weighting : A, Time-weighting : S

Toneburst : Frequency : 2 kHz, duration : 5 ms, period : 25 ms

(dB)				
Peak-to-rms ratio	Design goal	Indicated value	Difference	Tolerance limit
3.16	131.0	131.0	0.0	±0.5

7. Inherent noise level (dB)

(dB)		
Frequency weighting	Indicated value	Tolerance limit
A	10.0	17 or less
C	14.5	25 or less
Z	20.6	30 or less

8. Instrumental error

84.0 dB ± 0.7 dB 0.1 dB

Applicable standards

JIS C 1509-1 : 2005 Class 1
IEC 61672-1 : 2002 Class 1
ANSI S1.4-1983 Type 1
ANSI S1.43-1997 Type 1
CE marking (EMC Directive 2004/108/EC, Low Voltage Directive 2006/95/EC)
WEEE Directive (2002/96/EC)
Chinese RoHS

RION

Relative free field frequency response

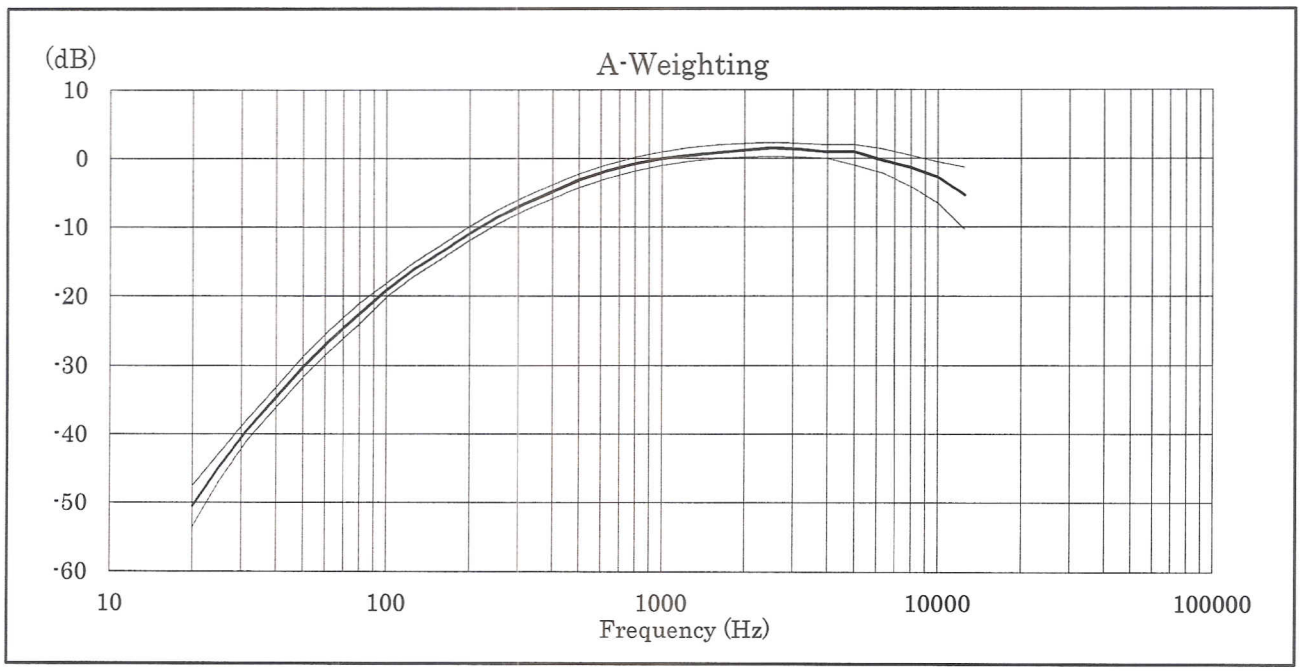

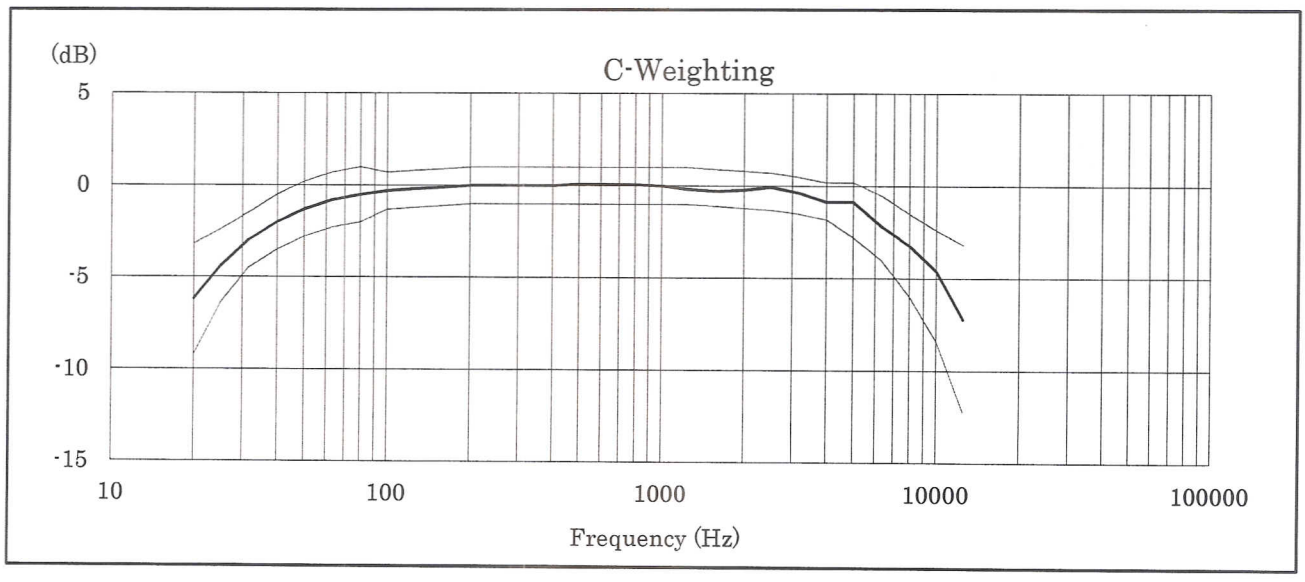

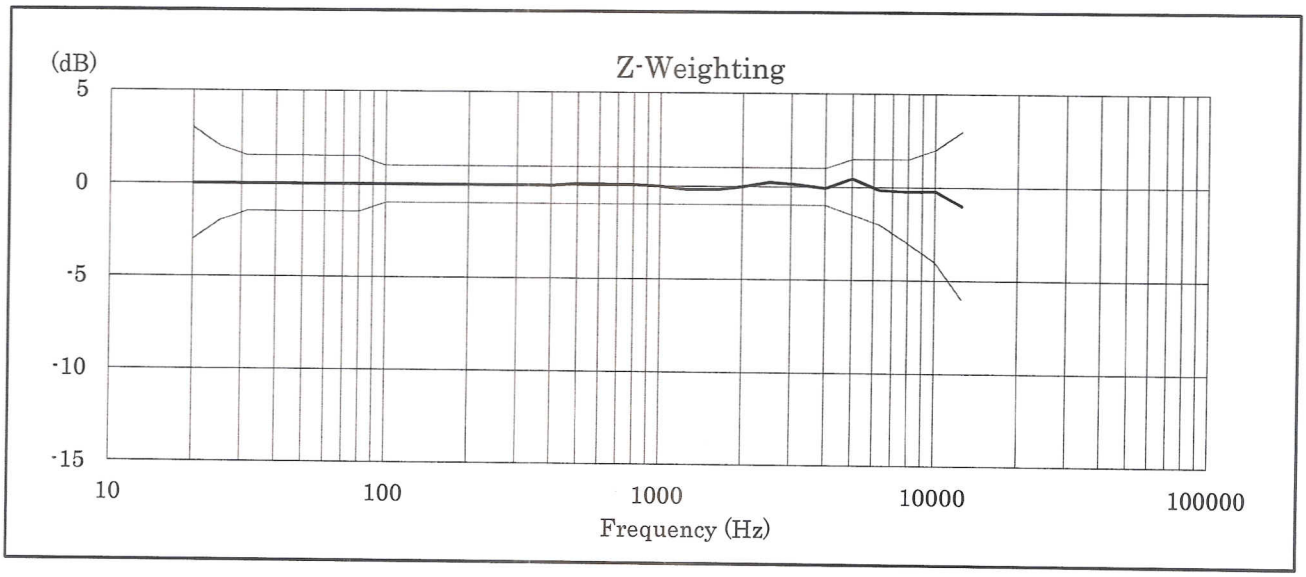

輝創工程有限公司
Sun Creation Engineering Limited
Calibration and Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C137684
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC13-3109)

Description / 儀器名稱	:	Sound Level Meter
Manufacturer / 製造商	:	Rion
Model No. / 型號	:	NL-52
Serial No. / 編號	:	00710259
Supplied By / 委託者	:	Envirotech Services Co. Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C
Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 3 December 2013

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By 測試 : K C Lee

Certified By 核證 : K M Wu

Date of Issue 簽發日期 : 4 December 2013

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里一號青山灣機樓四樓
Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Certificate of Calibration
校正證書

Certificate No. : C137684
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration using the Rion acoustic calibrator NC-73, S/N : 10486660 was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C130019
CL281	Multifunction Acoustic Calibrator	DC130171

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L_A	A	Fast	94.00	1	94.2	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L_A	A	Fast	94.00	1	94.2 (Ref.)
				104.00		104.2
				114.00		114.2

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L_A	A	Fast	94.00	1	94.2	Ref.
			Slow			94.2	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里一號青山灣機樓四樓
Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab@suncreation.com Website 網址: www.suncreation.com

Certificate of Calibration
校正證書

Certificate No. : C137684
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L_A	A	Fast	94.00	63 Hz	67.9	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.5
					250 Hz	85.5	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	95.5	+1.2 ± 1.6
					4 kHz	95.2	+1.0 ± 1.6
					8 kHz	93.2	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L_A	C	Fast	94.00	63 Hz	93.3	-0.8 ± 1.5
					125 Hz	94.0	-0.2 ± 1.5
					250 Hz	94.2	0.0 ± 1.4
					500 Hz	94.2	0.0 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	94.1	-0.2 ± 1.6
					4 kHz	93.4	-0.8 ± 1.6
					8 kHz	91.3	-3.0 (+2.1 ; -3.1)
					12.5 kHz	87.8	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 02695

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :
The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
G/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
香港新界屯門興安里一號青山灣機樓四樓
Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab@suncreation.com Website 網址: www.suncreation.com

輝創工程有限公司
Sun Creation Engineering Limited
Calibration and Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C134306
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC13-1709)

Description / 儀器名稱	:	Sound Level Calibrator
Manufacturer / 製造商	:	Rion
Model No. / 型號	:	NC-73
Serial No. / 編號	:	10786708
Supplied By / 委託者	:	Envirotech Services Co. Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C
Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 12 July 2013

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By 測試 : K C Lee

Certified By 核證 : K M Wu

Date of Issue 簽發日期 : 15 July 2013

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c o 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c o 香港新界屯門興安里一號青山灣機樓四樓
Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab@suncreation.com Website 網址: www.suncreation.com

Certificate of Calibration
校正證書

Certificate No. : C134306
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C133632
CL281	Multifunction Acoustic Calibrator	DC130171
TST150A	Measuring Amplifier	C120886

4. Test procedure : MA100N.

5. Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.8	± 0.5	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.990	1 kHz ± 2 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :
The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里一號青山灣機樓四樓
Tel 電話: 2927 2606 Fax 傳真: 2744 8986 E-mail 電郵: callab@suncreation.com Website 網址: www.suncreation.com

Appendix E
Calibration Record
(Water Quality Monitoring)

ALS Technichem (HK) Pty Ltd
11/F, Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung, N.T., Hong Kong
T: +852 2610 1044
F: +852 2610 2021
www.alsglobal.com

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR THOMAS WONG	**WORK ORDER:**	HK1334794
CLIENT:	ENOVATIVE ENVIRONMENTAL SERVICE LIMITED	**AMENDMENT NO.:**	1
ADDRESS:	RM 3704, SIK MAN HOUSE, HOMANTIN ESTATE, KOWLOON, HONG KONG	**LABORATORY:**	HONG KONG
		DATE RECEIVED:	13/12/2013
		DATE OF ISSUE:	27/12/2013
PROJECT:	--		

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of ALS will be followed.

Scope of Test:	Conductivity, Dissolved Oxygen, pH, Salinity and Temperature
Equipment Type:	Multimeter
Brand Name:	YSI
Model No.:	Professional Plus
Serial No.:	09K100735
Equipment No.:	--
Date of Calibration:	13 December, 2013

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee, Richard
General Manager -
Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

RIGHT SOLUTIONS | RIGHT PARTNER

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1334794
Amendment No.: 1
Date of Issue: 27/12/2013
Client: ENOVATIVE ENVIRONMENTAL SERVICE LIMITED

Description: Multimeter
Brand Name: YSI
Model No.: Professional Plus
Serial No.: 09K100735
Equipment No.: --
Date of Calibration: 13 December, 2013 Date of next Calibration: 13 March, 2014

Parameters:

Conductivity

Method Ref: APHA (21st edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	148.9	1.4
6667	6326	-5.1
12890	12227	-5.1
58670	54000	-8.0
	Tolerance Limit (±%)	10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.11	3.30	0.19
5.16	5.36	0.20
8.82	8.82	0.00
	Tolerance Limit (±mg/L)	0.20

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.20	0.20
7.0	7.16	0.16
10.0	10.06	0.06
	Tolerance Limit (±pH unit)	0.20

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	10.09	0.9
20	20.01	0.1
30	30.26	0.9
	Tolerance Limit (±%)	10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard
General Manager -
Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1334794
Amendment No.: 1
Date of Issue: 27/12/2013
Client: ENOVATIVE ENVIRONMENTAL SERVICE LIMITED

Description: Multimeter
Brand Name: YSI
Model No.: Professional Plus
Serial No.: 09K100735
Equipment No.: --
Date of Calibration: 13 December, 2013 Date of next Calibration: 13 March, 2014

Parameters:

Temperature **Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.**

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
9.0	8.4	-0.6
20.0	19.6	-0.4
38.0	38.3	0.3
	Tolerance Limit (±°C)	2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard
General Manager -
Greater China & Hong Kong

ALS Technichem (HK) Pty Ltd
11/F, Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung, N.T., Hong Kong
T: +852 2610 1044
F: +852 2610 2021
www.alsglobal.com

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	MR THOMAS WONG	**WORK ORDER:**	HK1334790
CLIENT:	ENOVATIVE ENVIRONMENTAL SERVICE LIMITED	**LABORATORY:**	HONG KONG
ADDRESS:	RM 3704, SIK MAN HOUSE, HOMANTIN ESTATE, KOWLOON, HONG KONG	**DATE RECEIVED:**	13/12/2013
		DATE OF ISSUE:	27/12/2013
PROJECT:			

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Scope of Test:	Turbidity
Description:	Turbidimeter
Brand Name:	HACH
Model No.:	2100Q is
Serial No.:	11050C001264
Equipment No.:	--
Date of Calibration:	20 December, 2013

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee Richard
General Manager
Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1334790
Date of Issue: 27/12/2013
Client: ENOVATIVE ENVIRONMENTAL SERVICE LIMITED

Description: Turbidimeter
Brand Name: HACH
Model No.: 2100Q is
Serial No.: 11050C001264
Equipment No.: --
Date of Calibration: 20 December, 2013 Date of next Calibration: 20 March, 2014

Parameters:

Turbidity

Method Ref: APHA 21st Ed. 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.86	--
4	3.85	-3.8
40	36.7	-8.2
80	84.1	5.1
400	389	-2.8
800	813	1.6
	Tolerance Limit (±%)	10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard
General Manager -
Greater China & Hong Kong

Appendix F. Graphical Plots of the Monitoring Results

Air Quality

1-hour TSP Level at ASR1

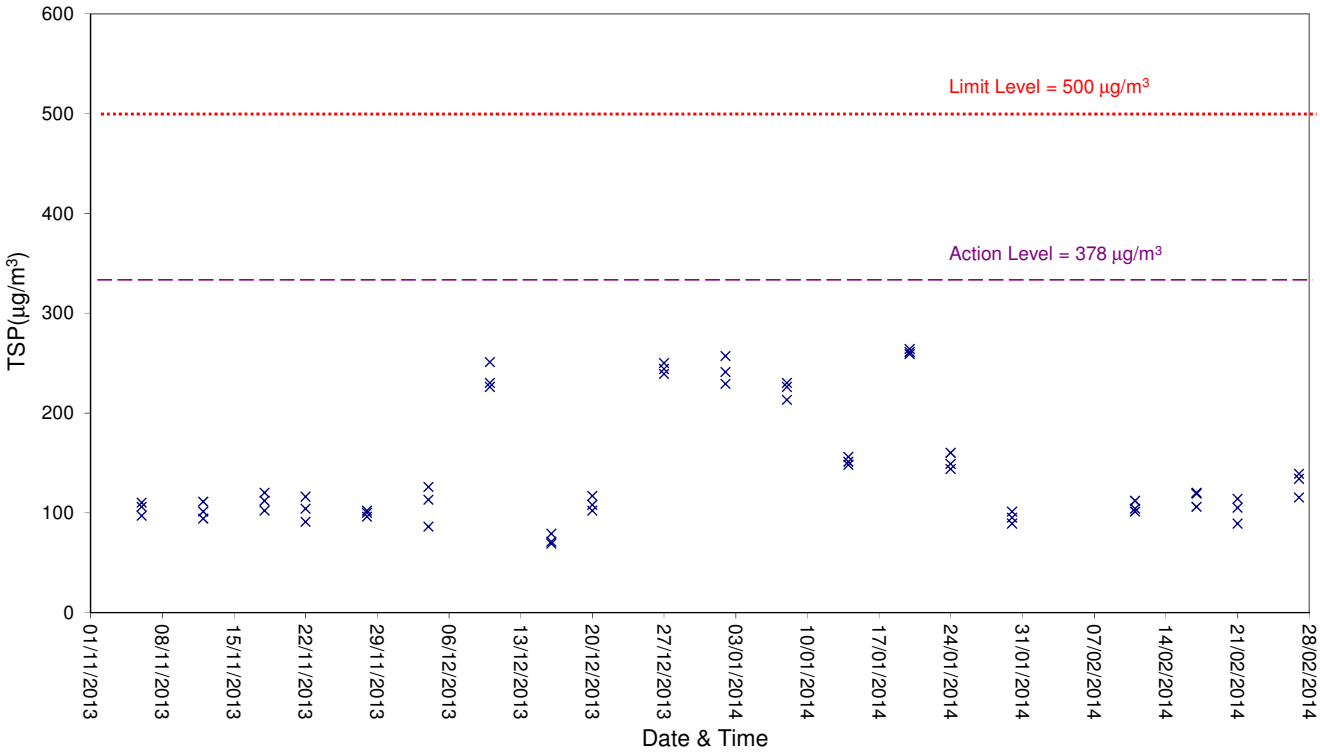

1-hour TSP Level at ASR2A

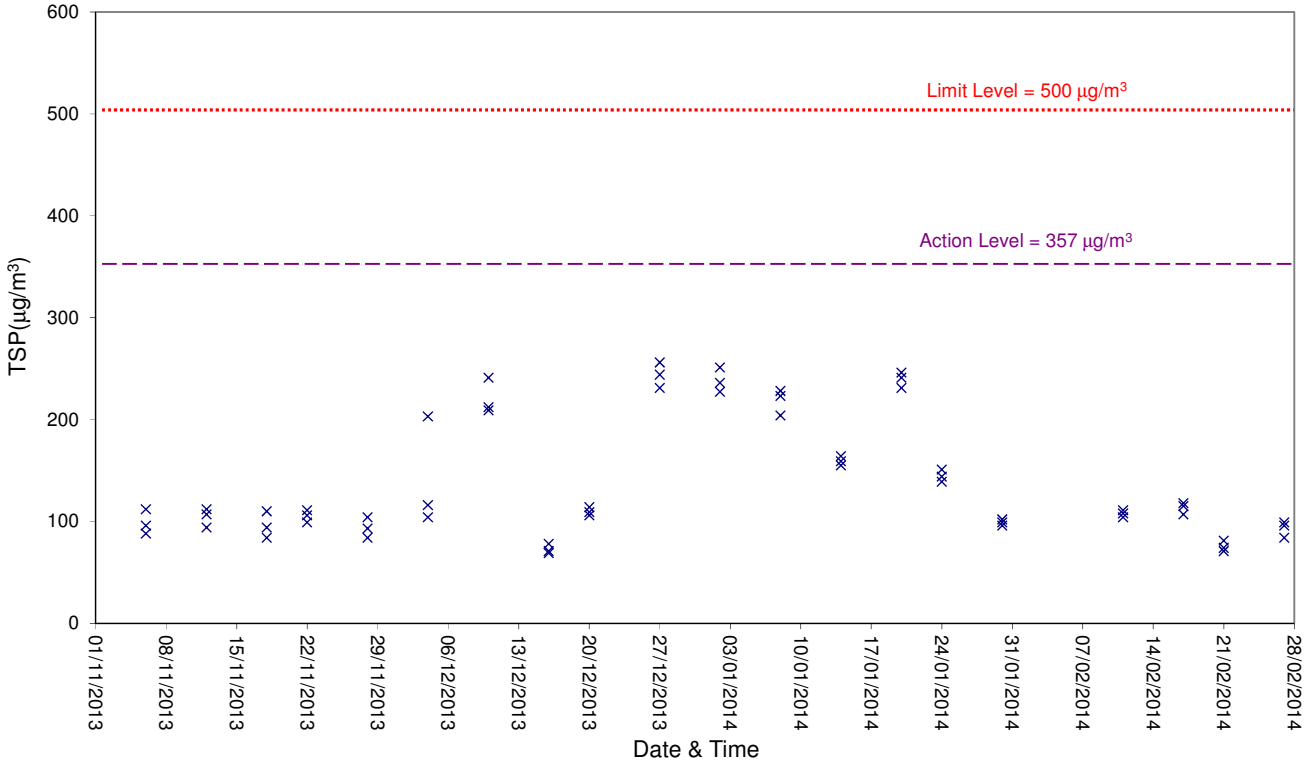

Air Quality

1-hour TSP Level at ASR3

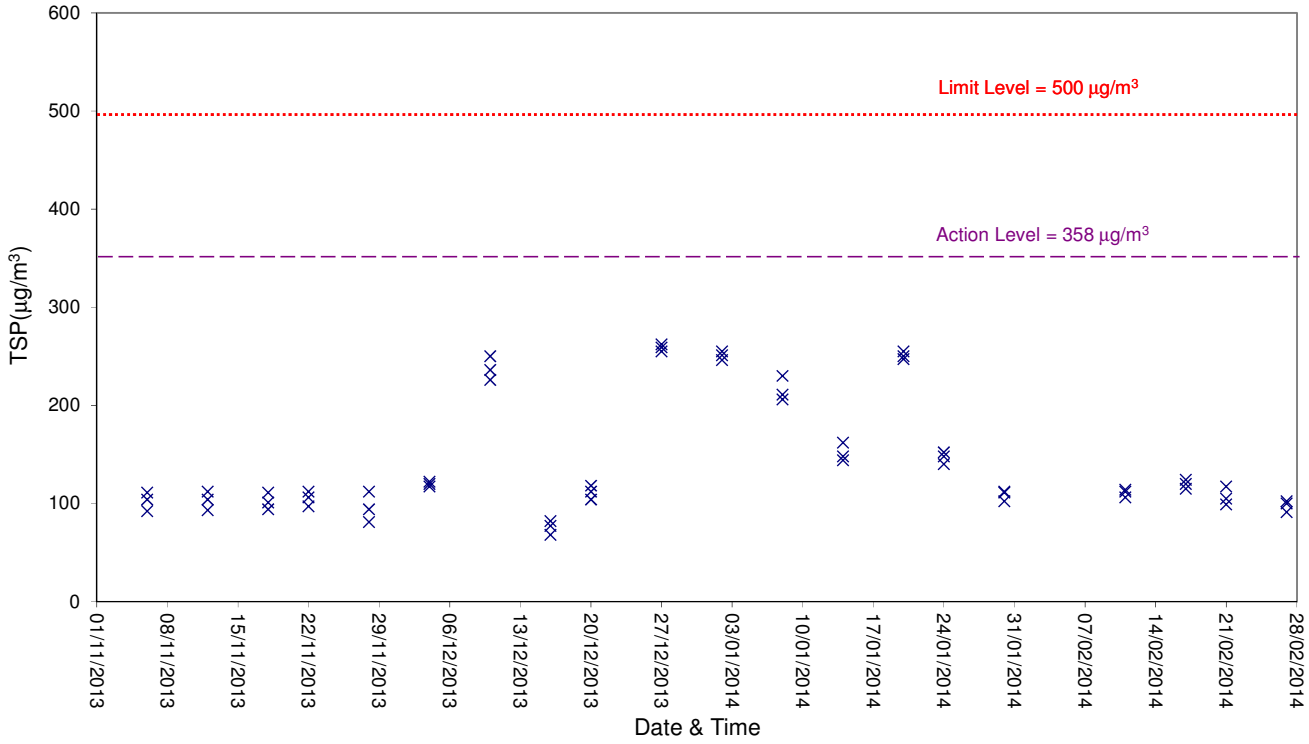

1-hour TSP Level at ASR4

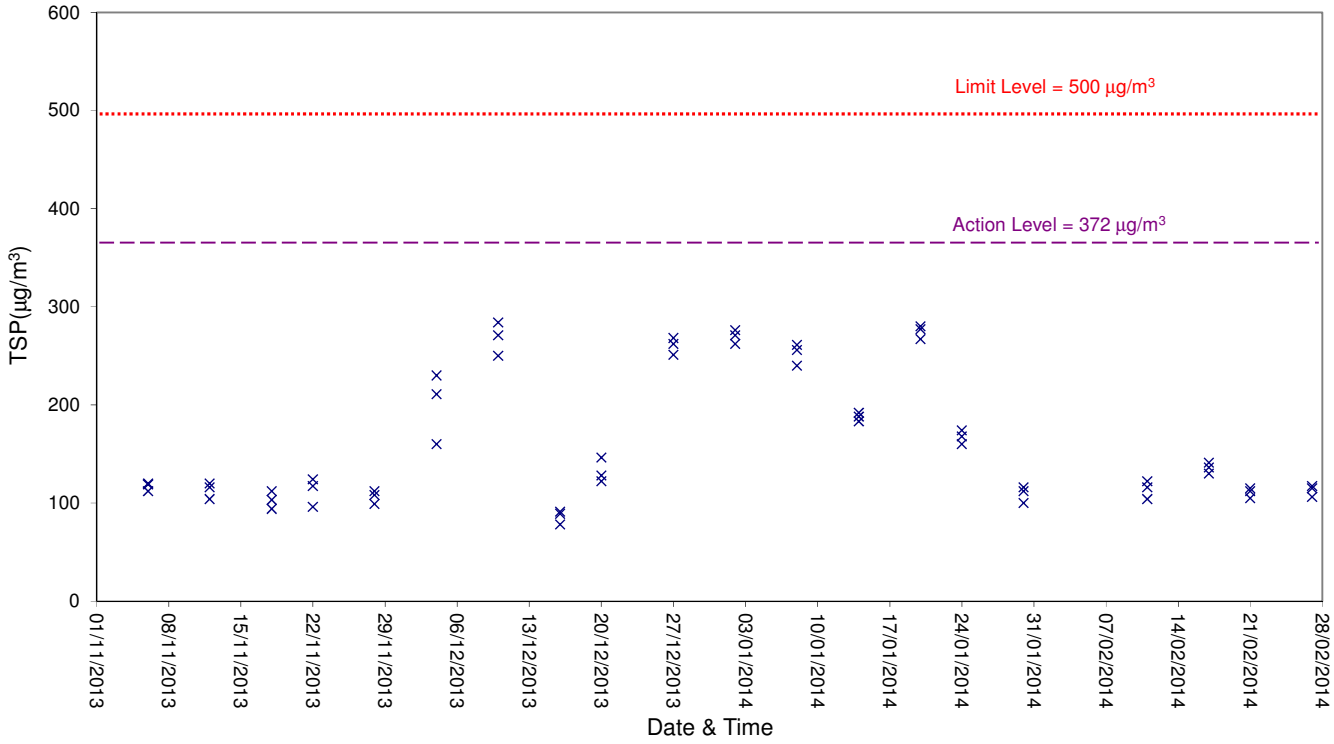

Air Quality

24-hour TSP Level at ASR1

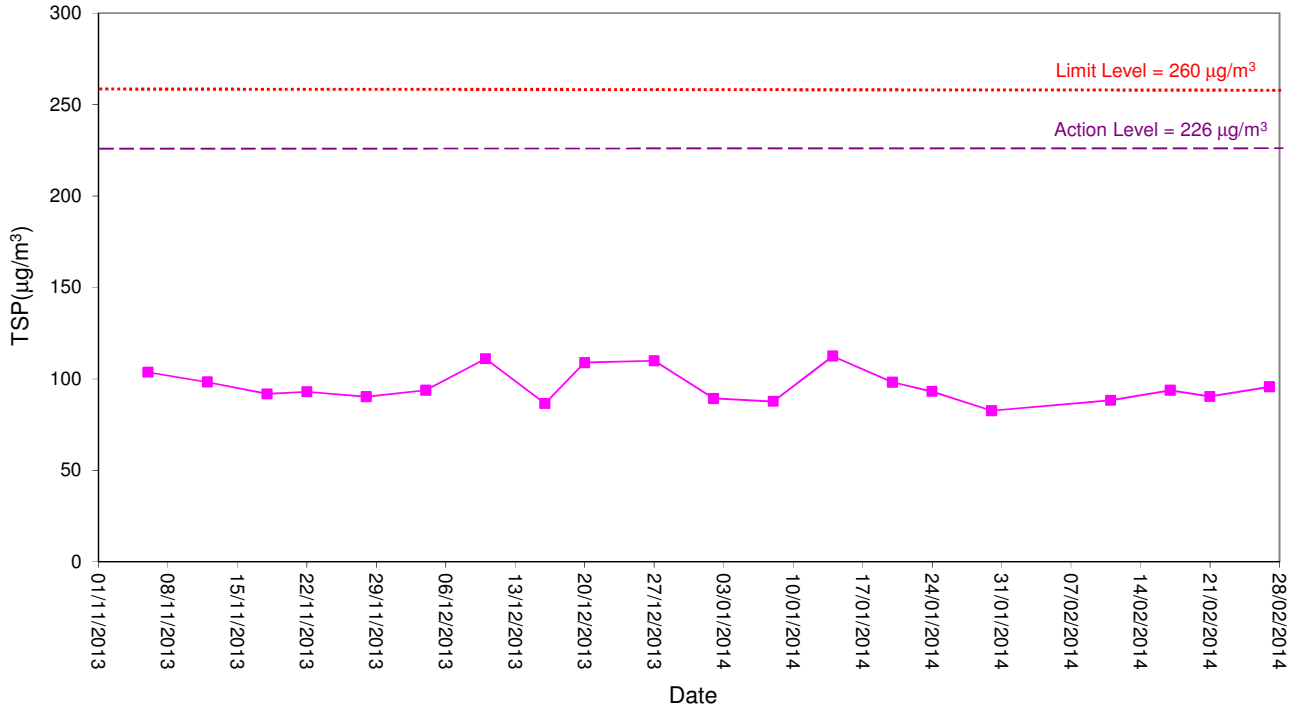

24-hour TSP Level at ASR2A

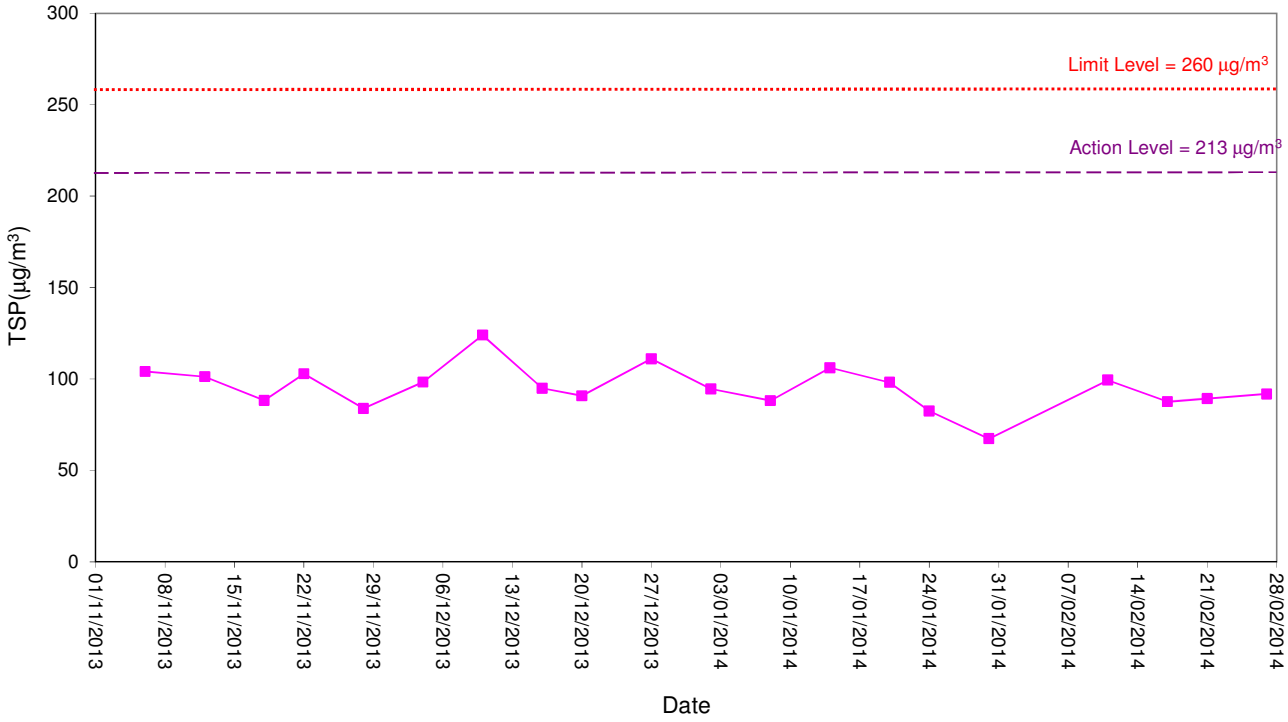

Air Quality

24-hour TSP Level at ASR3

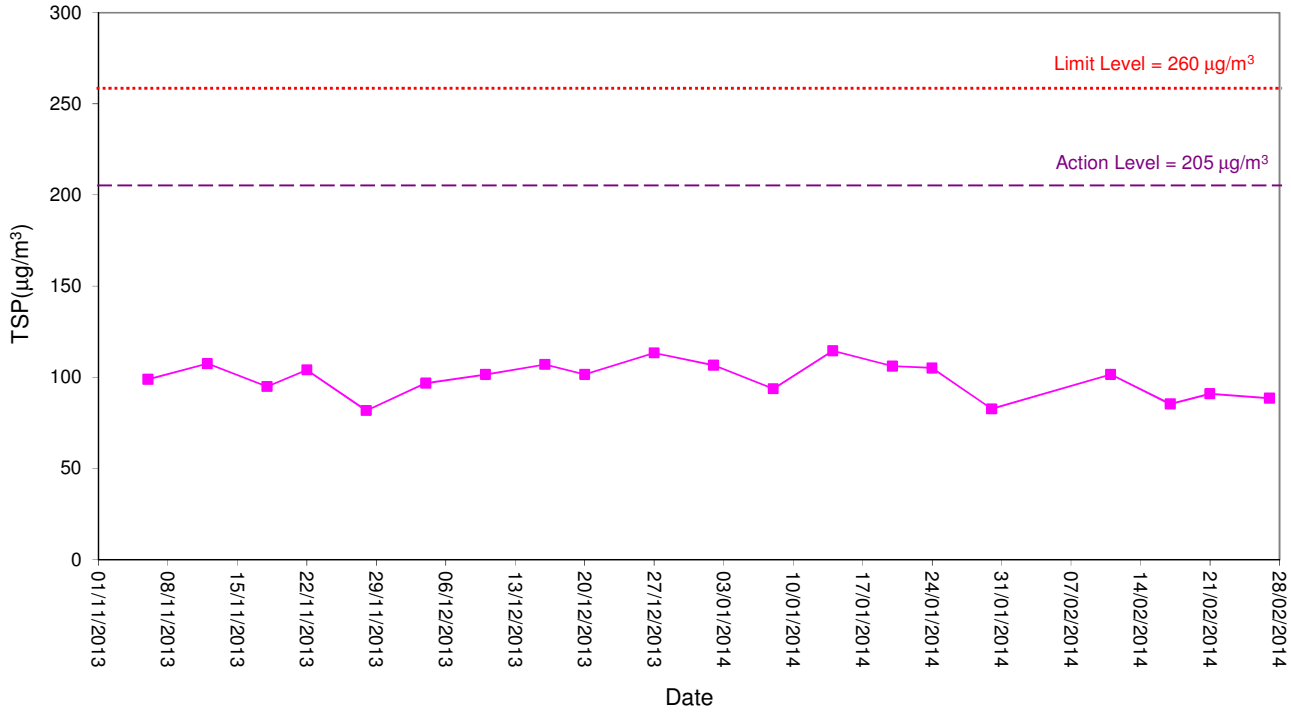

24-hour TSP Level at ASR4

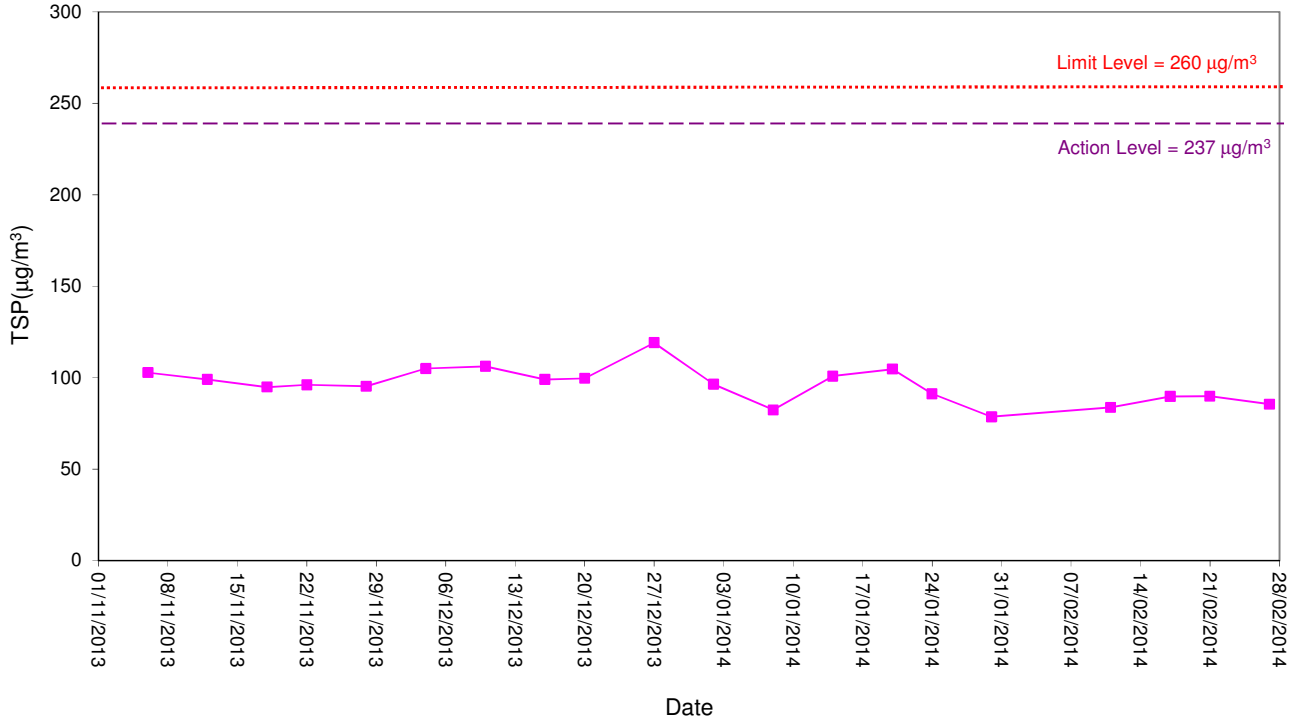

Noise

Noise Level for 30 min, dB(A), at NSR1

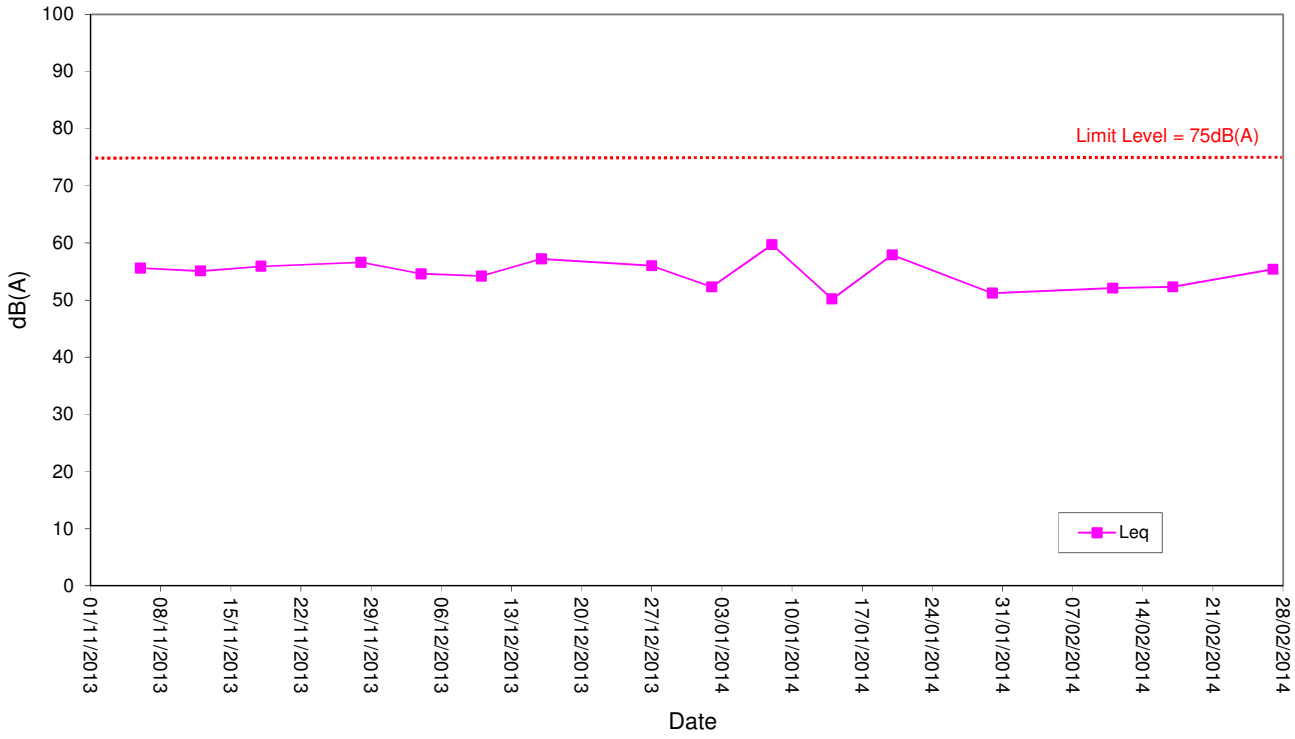

Noise Level for 30 min, dB(A), at NSR3

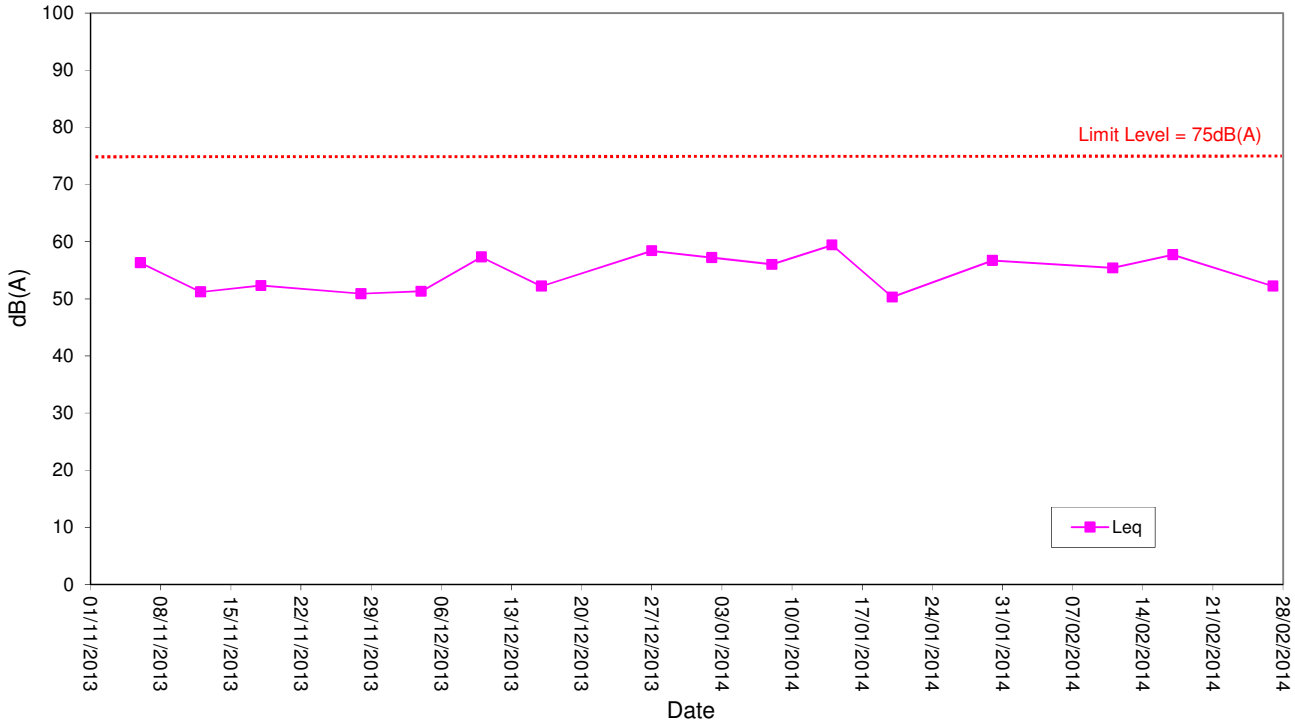

Noise

Noise Level for 30 min, dB(A), at NSR5

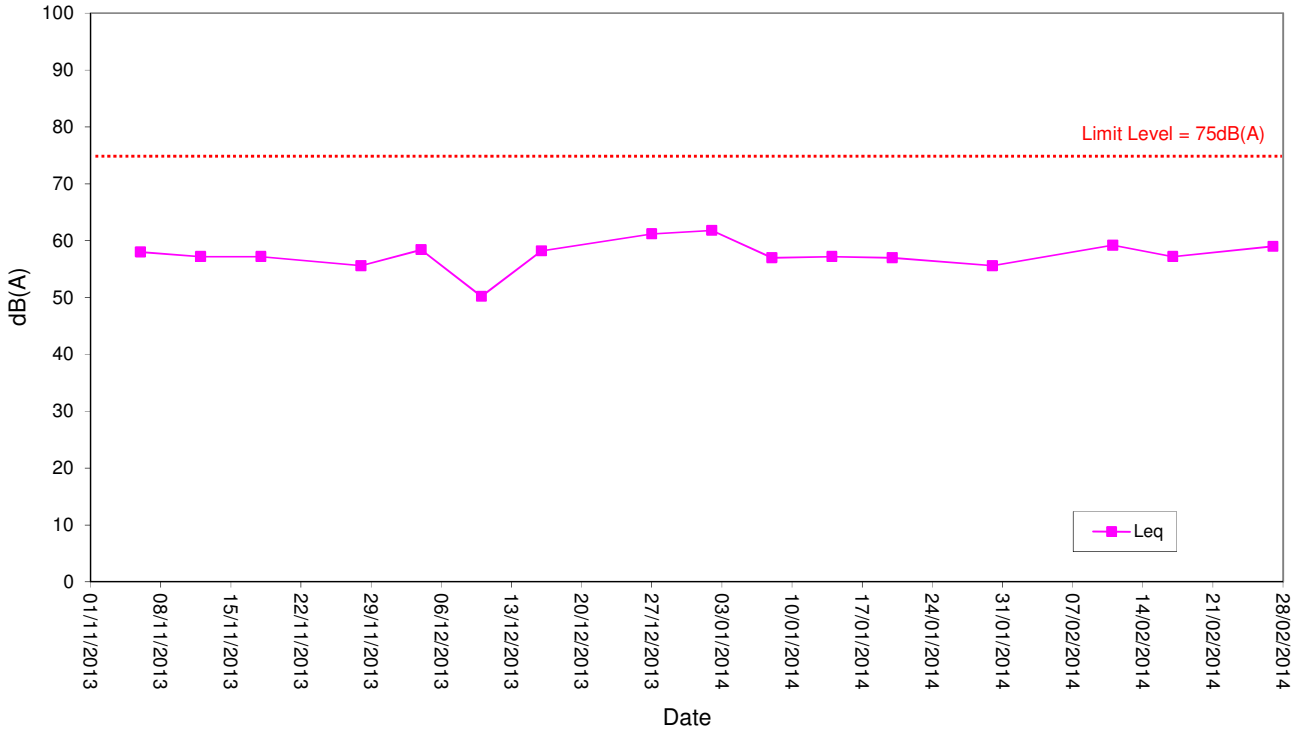

Noise Level for 30 min, dB(A), at NSR7

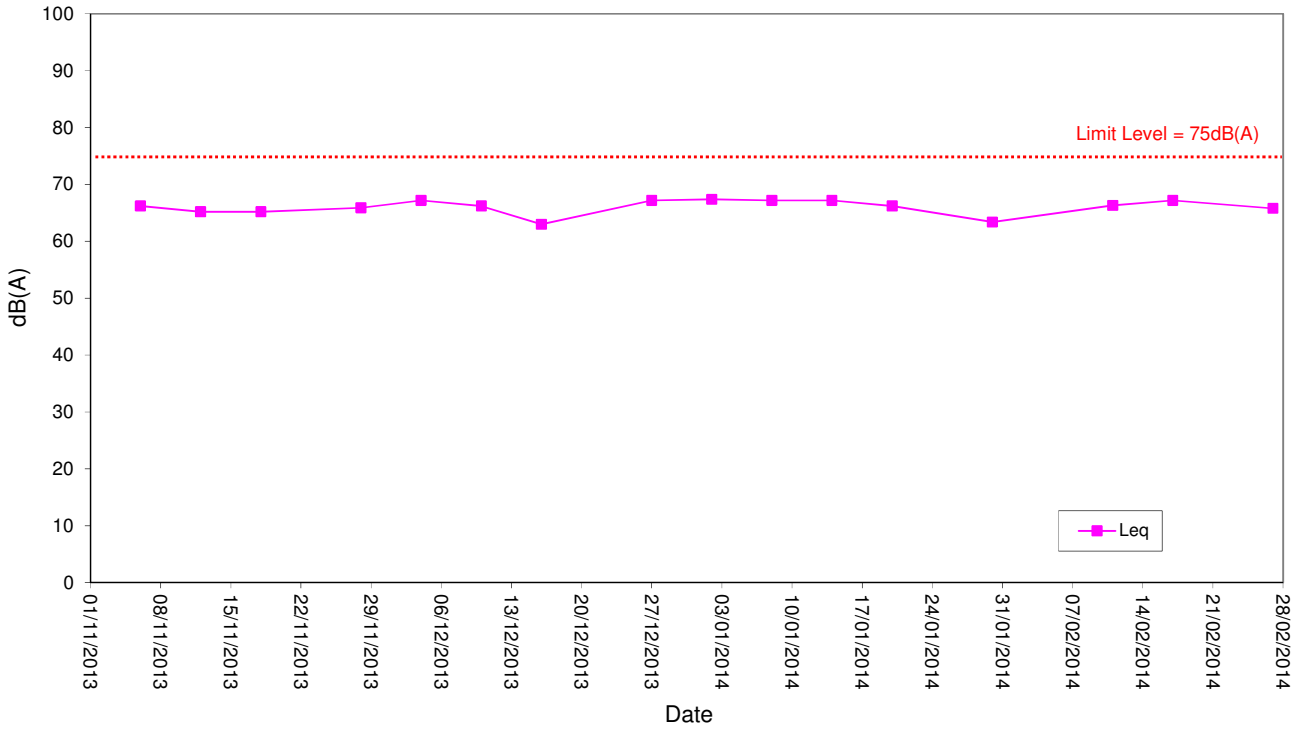

Water Quality

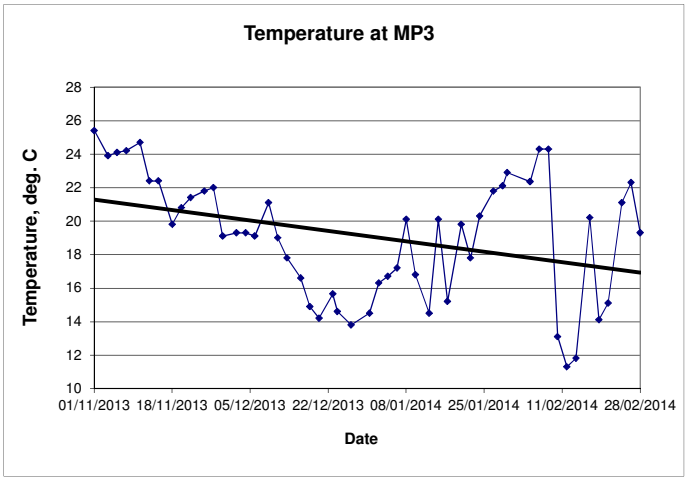

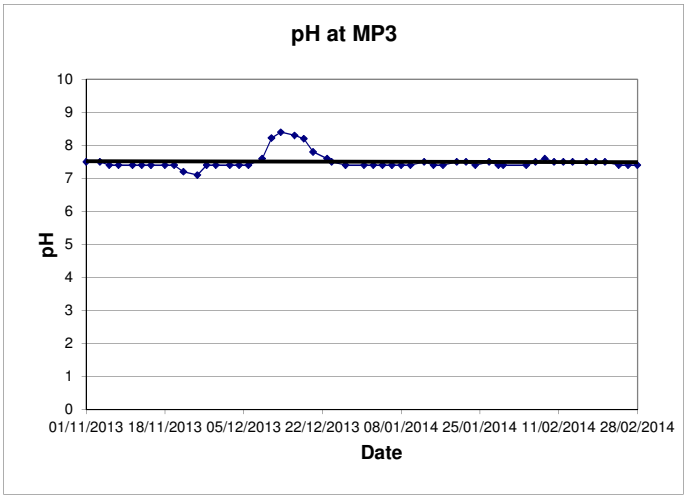

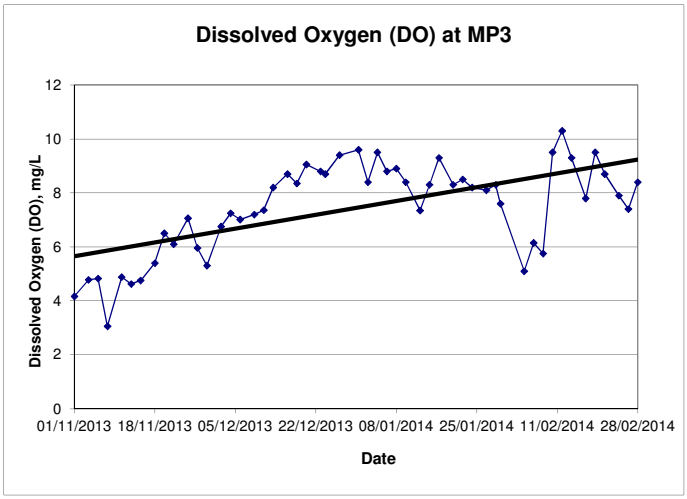

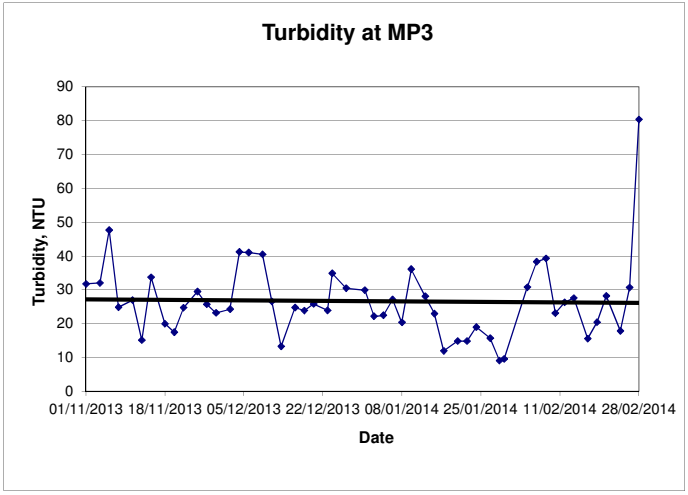

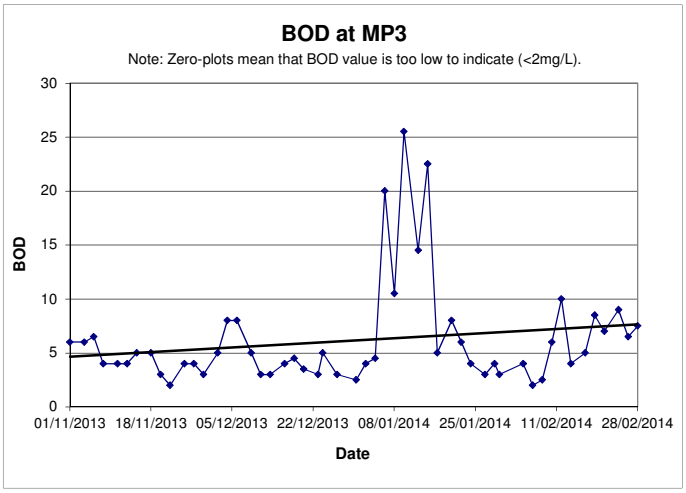

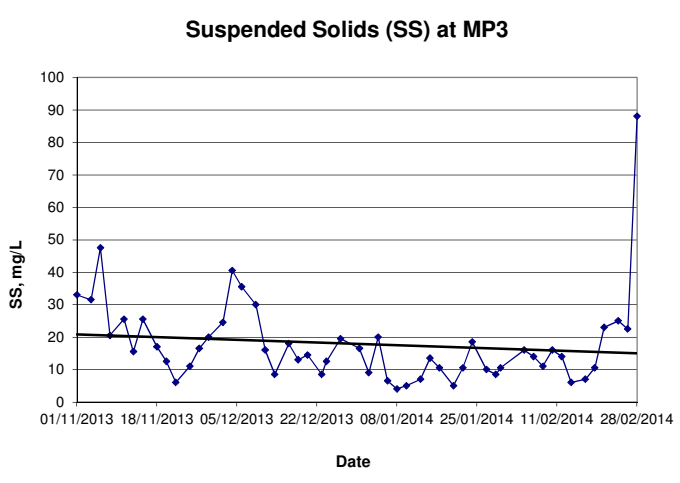

Water Quality

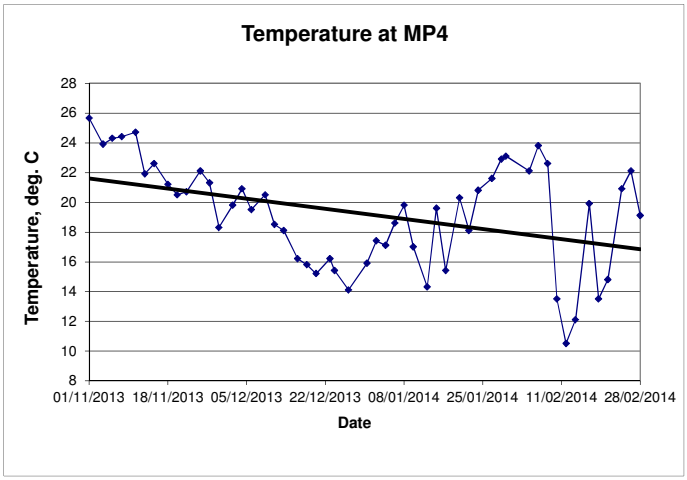

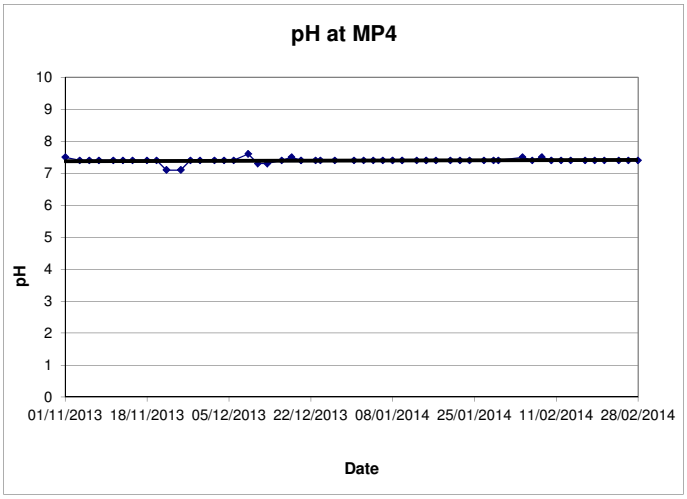

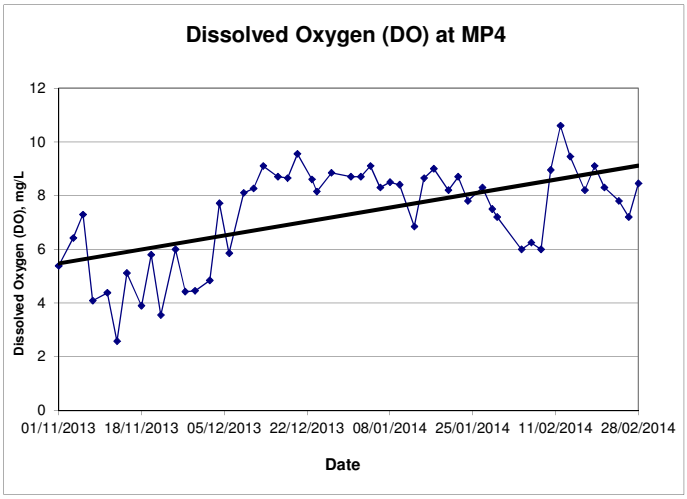

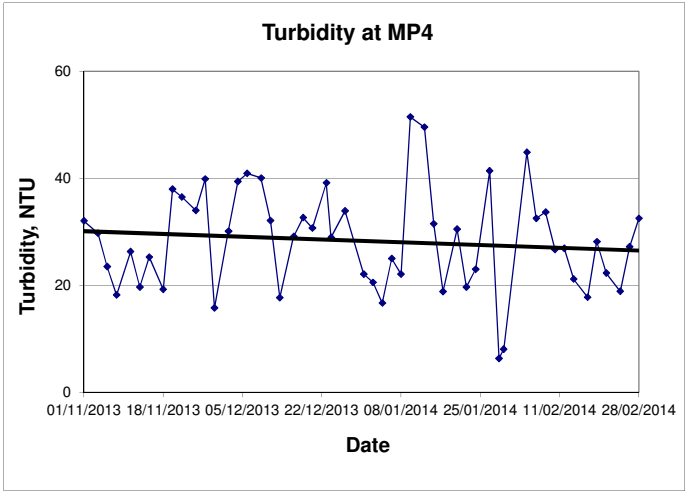

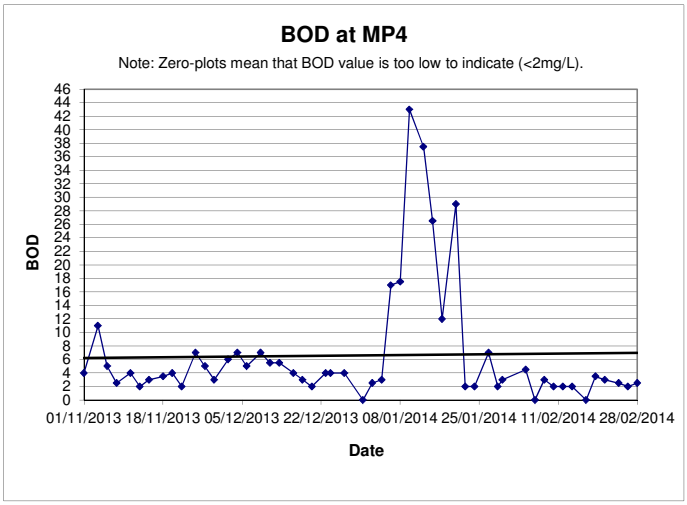

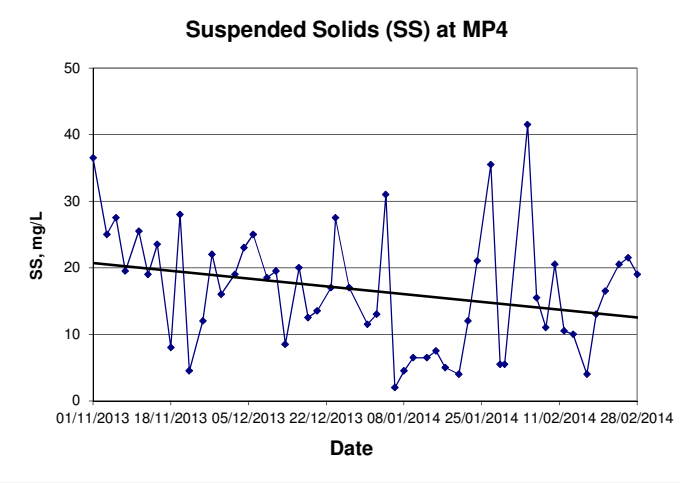

Water Quality

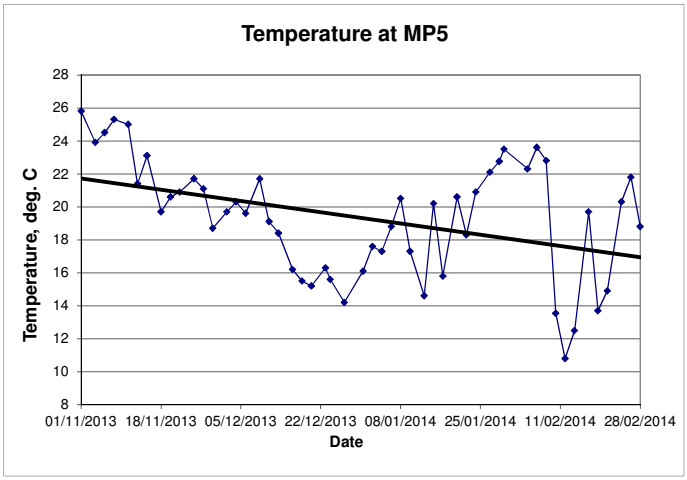

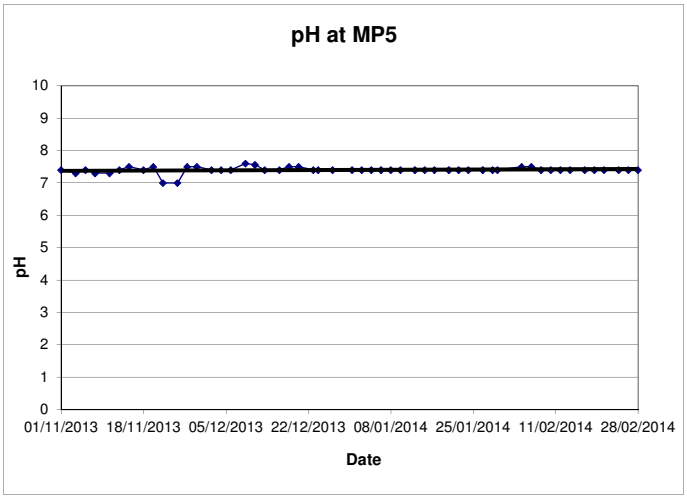

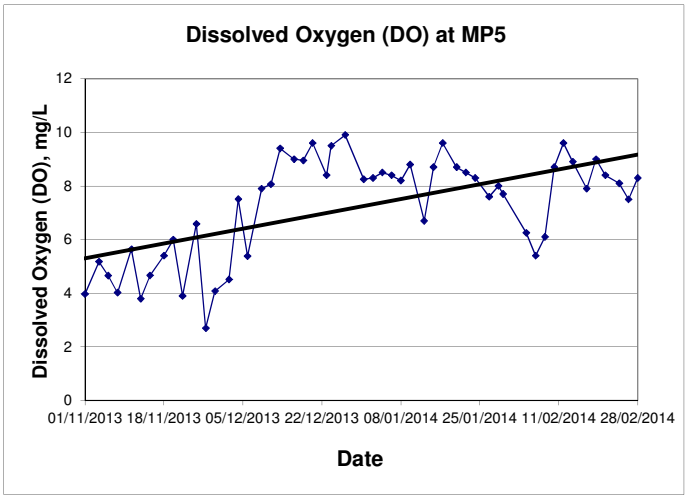

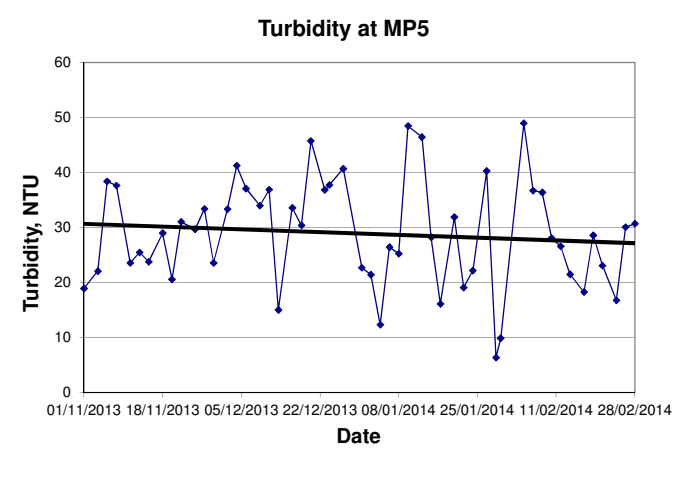

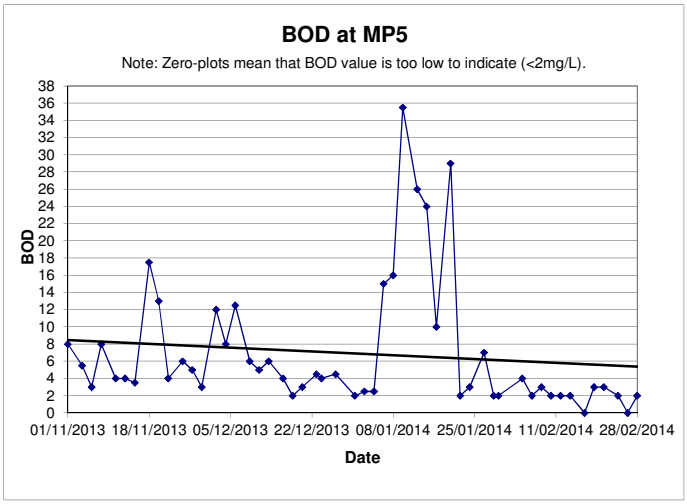

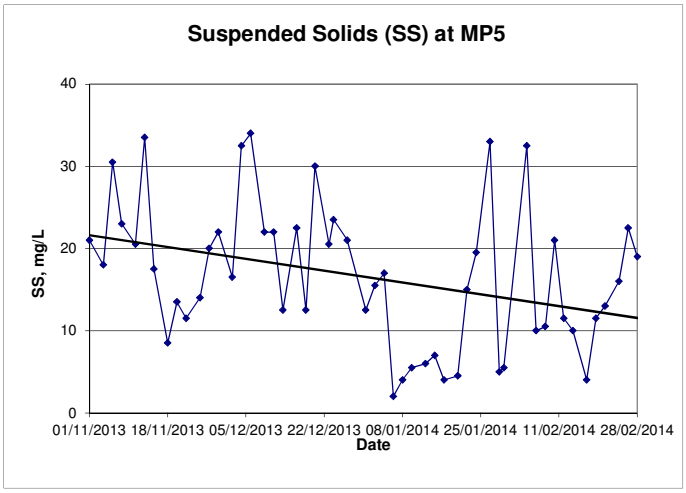

Water Quality

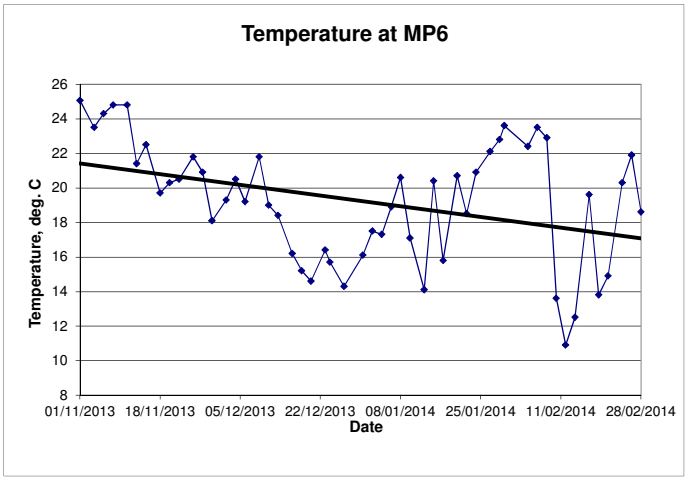

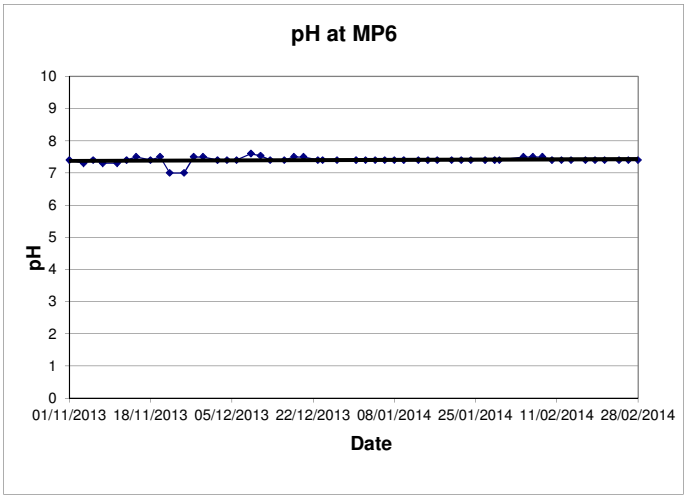

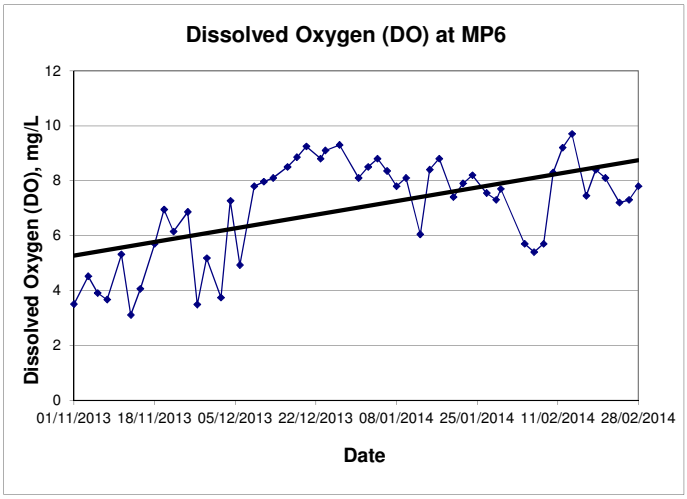

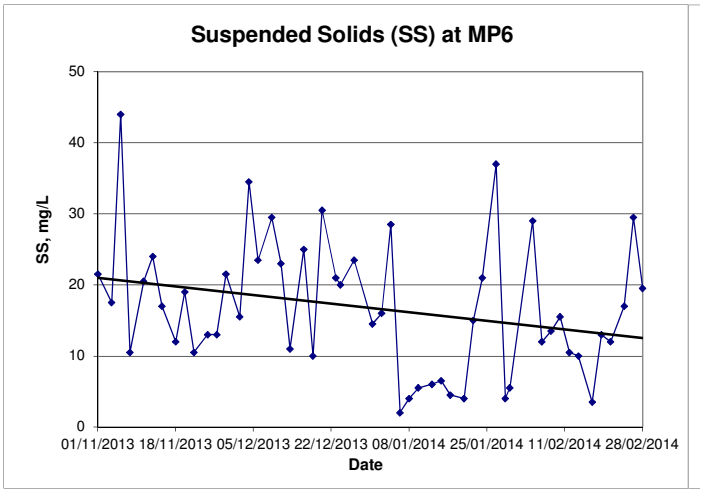

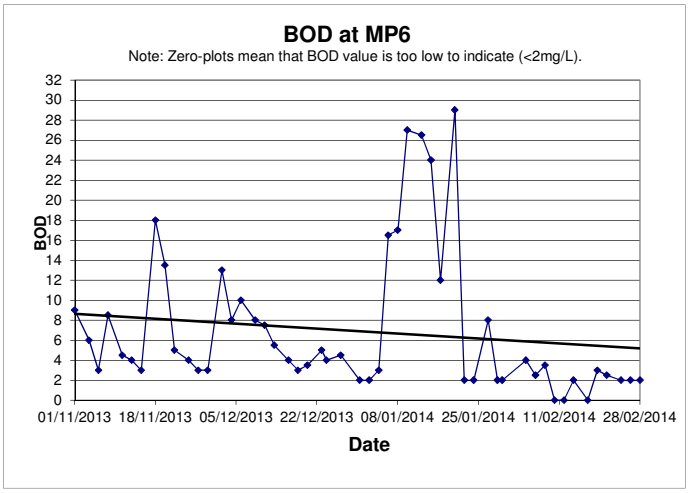

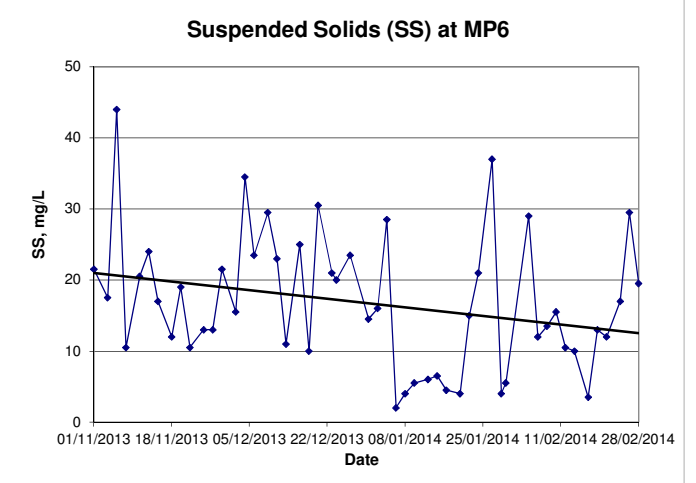

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1403188**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **04-FEB-2014**		
Order number	: **----**			*Date of issue*	: **13-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1403188 supersedes any previous reports with this reference. The completion date of analysis is 07-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1403188 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
			LOR Unit	2 mg/L	2 mg/L			
				EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[04-FEB-2014]	HK1403188-001		**15**	**4**			
MP3-2	[04-FEB-2014]	HK1403188-002		**15**	**4**			
MP4-1	[04-FEB-2014]	HK1403188-003		**43**	**4**			
MP4-2	[04-FEB-2014]	HK1403188-004		**40**	**5**			
MP5-1	[04-FEB-2014]	HK1403188-005		**32**	**4**			
MP5-2	[04-FEB-2014]	HK1403188-006		**33**	**4**			
MP6-1	[04-FEB-2014]	HK1403188-007		**29**	**4**			
MP6-2	[04-FEB-2014]	HK1403188-008		**29**	**4**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3281962)								
HK1403124-005	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK1403188-008	MP6-2	EA025: Suspended Solids (SS)	----	2	mg/L	29	28	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3281962)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3284510)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	91.4	----	78	112	----	----
EP: Aggregate Organics (QCLot: 3284512)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	92.9	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1403561**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **07-FEB-2014**		
Order number	: **----**			*Date of issue*	: **18-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1403561 supersedes any previous reports with this reference. The completion date of analysis is 12-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1403561 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[06-FEB-2014]	HK1403561-001	**14**	**2**			
MP3-2	[06-FEB-2014]	HK1403561-002	**14**	**2**			
MP4-1	[06-FEB-2014]	HK1403561-003	**16**	<2			
MP4-2	[06-FEB-2014]	HK1403561-004	**15**	<2			
MP5-1	[06-FEB-2014]	HK1403561-005	**10**	**2**			
MP5-2	[06-FEB-2014]	HK1403561-006	**10**	<2			
MP6-1	[06-FEB-2014]	HK1403561-007	**12**	**2**			
MP6-2	[06-FEB-2014]	HK1403561-008	**12**	**3**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3286733)								
HK1403524-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK1403541-003	Anonymous	EA025: Suspended Solids (SS)	----	1	mg/L	<1	<1	0.0
EA/ED: Physical and Aggregate Properties (QC Lot: 3286734)								
HK1403561-004	MP4-2	EA025: Suspended Solids (SS)	----	2	mg/L	15	16	0.0
HK1403562-006	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	3	3	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3286733)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	97.5	----	87	111	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 3286734)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	101	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3287420)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	93.3	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1403774**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **10-FEB-2014**		
Order number	: **----**			*Date of issue*	: **19-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1403774 supersedes any previous reports with this reference. The completion date of analysis is 12-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1403774 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
			LOR Unit	2 mg/L	2 mg/L			
				EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[08-FEB-2014]	HK1403774-001		**11**	**3**			
MP3-2	[08-FEB-2014]	HK1403774-002		**11**	**2**			
MP4-1	[08-FEB-2014]	HK1403774-003		**11**	**3**			
MP4-2	[08-FEB-2014]	HK1403774-004		**11**	**3**			
MP5-1	[08-FEB-2014]	HK1403774-005		**10**	**3**			
MP5-2	[08-FEB-2014]	HK1403774-006		**11**	**3**			
MP6-1	[08-FEB-2014]	HK1403774-007		**13**	**4**			
MP6-2	[08-FEB-2014]	HK1403774-008		**14**	**3**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3287969)								
HK1403752-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	43	44	2.8
HK1403774-001	MP3-1	EA025: Suspended Solids (SS)	----	2	mg/L	11	11	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3287969)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3290998)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	92.4	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1403775**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **10-FEB-2014**		
Order number	: **----**			*Date of issue*	: **19-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1403775 supersedes any previous reports with this reference. The completion date of analysis is 12-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1403775 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[10-FEB-2014]	HK1403775-001	**16**	**6**			
MP3-2	[10-FEB-2014]	HK1403775-002	**16**	**6**			
MP4-1	[10-FEB-2014]	HK1403775-003	**21**	**2**			
MP4-2	[10-FEB-2014]	HK1403775-004	**20**	**2**			
MP5-1	[10-FEB-2014]	HK1403775-005	**21**	**2**			
MP5-2	[10-FEB-2014]	HK1403775-006	**21**	<2			
MP6-1	[10-FEB-2014]	HK1403775-007	**15**	<2			
MP6-2	[10-FEB-2014]	HK1403775-008	**16**	<2			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3287969)								
HK1403752-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	43	44	2.8
HK1403774-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	11	11	0.0
EA/ED: Physical and Aggregate Properties (QC Lot: 3287970)								
HK1403775-003	MP4-1	EA025: Suspended Solids (SS)	----	2	mg/L	21	20	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3287969)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	87	111	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 3287970)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	98.0	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3290998)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	92.4	----	78	112	----	----
EP: Aggregate Organics (QCLot: 3291000)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	92.4	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1404224**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **12-FEB-2014**		
Order number	: **----**			*Date of issue*	: **21-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1404224 supersedes any previous reports with this reference. The completion date of analysis is 17-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1404224 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[12-FEB-2014]	HK1404224-001	**14**	**10**			
MP3-2	[12-FEB-2014]	HK1404224-002	**14**	**10**			
MP4-1	[12-FEB-2014]	HK1404224-003	**10**	**2**			
MP4-2	[12-FEB-2014]	HK1404224-004	**11**	**2**			
MP5-1	[12-FEB-2014]	HK1404224-005	**11**	**2**			
MP5-2	[12-FEB-2014]	HK1404224-006	**12**	**2**			
MP6-1	[12-FEB-2014]	HK1404224-007	**11**	<2			
MP6-2	[12-FEB-2014]	HK1404224-008	**10**	<2			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3293079)								
HK1404222-003	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	7	7	0.0
HK1404224-007	MP6-1	EA025: Suspended Solids (SS)	----	2	mg/L	11	11	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3293079)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	98.5	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3296106)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	94.5	----	78	112	----	----
EP: Aggregate Organics (QCLot: 3296107)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	86.7	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	: ALS Technichem HK Pty Ltd	Page	: 1 of 3		
Contact	: MR THOMAS WONG	Contact	: Fung Lim Chee, Richard	Work Order	: HK1404673		
Address	: RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG	Address	: 11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong				
E-mail	: Thomas.wong@eno.com.hk	E-mail	: Richard.Fung@alsglobal.com				
Telephone	: ----	Telephone	: +852 2610 1044				
Facsimile	: ----	Facsimile	: +852 2610 2021				
Project	: PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG	Quote number	: HK/1577/2009**	Date received	: 14-FEB-2014		
Order number	: ----			Date of issue	: 25-FEB-2014		
C-O-C number	: ----			No. of samples	- Received :	8	
Site	: ----				- Analysed :	8	

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1404673 supersedes any previous reports with this reference. The completion date of analysis is 20-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1404673 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[14-FEB-2014]	HK1404673-001	**6**	**4**			
MP3-2	[14-FEB-2014]	HK1404673-002	**6**	**4**			
MP4-1	[14-FEB-2014]	HK1404673-003	**10**	**2**			
MP4-2	[14-FEB-2014]	HK1404673-004	**11**	**2**			
MP5-1	[14-FEB-2014]	HK1404673-005	**10**	<2			
MP5-2	[14-FEB-2014]	HK1404673-006	**10**	**2**			
MP6-1	[14-FEB-2014]	HK1404673-007	**10**	<2			
MP6-2	[14-FEB-2014]	HK1404673-008	**10**	**2**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3297665)								
HK1404570-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	5	5	0.0
HK1404626-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
EA/ED: Physical and Aggregate Properties (QC Lot: 3297666)								
HK1404673-003	MP4-1	EA025: Suspended Solids (SS)	----	2	mg/L	10	10	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3297665)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	102	----	87	111	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 3297666)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	102	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3298563)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	95.2	----	78	112	----	----
EP: Aggregate Organics (QCLot: 3298564)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	94.7	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1404983**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **17-FEB-2014**		
Order number	: **----**			*Date of issue*	: **26-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1404983 supersedes any previous reports with this reference. The completion date of analysis is 24-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1404983 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
			LOR Unit	2 mg/L	2 mg/L			
				EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[17-FEB-2014]	HK1404983-001		**8**	**5**			
MP3-2	[17-FEB-2014]	HK1404983-002		**6**	**5**			
MP4-1	[17-FEB-2014]	HK1404983-003		**4**	<2			
MP4-2	[17-FEB-2014]	HK1404983-004		**4**	<2			
MP5-1	[17-FEB-2014]	HK1404983-005		**4**	<2			
MP5-2	[17-FEB-2014]	HK1404983-006		**4**	<2			
MP6-1	[17-FEB-2014]	HK1404983-007		**4**	<2			
MP6-2	[17-FEB-2014]	HK1404983-008		**3**	<2			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3302141)								
HK1404959-005	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	2	2	0.0
HK1404983-002	MP3-2	EA025: Suspended Solids (SS)	----	2	mg/L	6	6	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3302141)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3303580)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	101	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1405271**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **19-FEB-2014**		
Order number	: **----**			*Date of issue*	: **27-FEB-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1405271 supersedes any previous reports with this reference. The completion date of analysis is 24-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1405271 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[19-FEB-2014]	HK1405271-001	**10**	**8**			
MP3-2	[19-FEB-2014]	HK1405271-002	**11**	**9**			
MP4-1	[19-FEB-2014]	HK1405271-003	**13**	**4**			
MP4-2	[19-FEB-2014]	HK1405271-004	**13**	**3**			
MP5-1	[19-FEB-2014]	HK1405271-005	**11**	**3**			
MP5-2	[19-FEB-2014]	HK1405271-006	**12**	**3**			
MP6-1	[19-FEB-2014]	HK1405271-007	**13**	**3**			
MP6-2	[19-FEB-2014]	HK1405271-008	**13**	**3**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3305702)								
HK1405231-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	6	6	0.0
HK1405248-007	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	169	174	2.6
EA/ED: Physical and Aggregate Properties (QC Lot: 3305703)								
HK1405271-003	MP4-1	EA025: Suspended Solids (SS)	----	2	mg/L	13	12	0.0
HK1405277-005	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	7	6	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3305702)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	97.5	----	87	111	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 3305703)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3306980)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	97.7	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1405558**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **21-FEB-2014**		
Order number	: **----**			*Date of issue*	: **03-MAR-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1405558 supersedes any previous reports with this reference. The completion date of analysis is 26-FEB-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1405558 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[21-FEB-2014]	HK1405558-001	**23**	**7**			
MP3-2	[21-FEB-2014]	HK1405558-002	**23**	**7**			
MP4-1	[21-FEB-2014]	HK1405558-003	**17**	**3**			
MP4-2	[21-FEB-2014]	HK1405558-004	**16**	**3**			
MP5-1	[21-FEB-2014]	HK1405558-005	**13**	**3**			
MP5-2	[21-FEB-2014]	HK1405558-006	**13**	**3**			
MP6-1	[21-FEB-2014]	HK1405558-007	**12**	**2**			
MP6-2	[21-FEB-2014]	HK1405558-008	**12**	**3**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3310186)								
HK1405550-004	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK1405558-004	MP4-2	EA025: Suspended Solids (SS)	----	2	mg/L	16	15	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3310186)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	98.5	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3309809)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	91.7	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1405715**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **24-FEB-2014**		
Order number	: **----**			*Date of issue*	: **04-MAR-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1405715 supersedes any previous reports with this reference. The completion date of analysis is 03-MAR-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1405715 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
			LOR Unit	2 mg/L	2 mg/L			
				EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[24-FEB-2014]	HK1405715-001		**26**	**9**			
MP3-2	[24-FEB-2014]	HK1405715-002		**24**	**9**			
MP4-1	[24-FEB-2014]	HK1405715-003		**20**	**3**			
MP4-2	[24-FEB-2014]	HK1405715-004		**21**	**2**			
MP5-1	[24-FEB-2014]	HK1405715-005		**16**	**2**			
MP5-2	[24-FEB-2014]	HK1405715-006		**16**	<2			
MP6-1	[24-FEB-2014]	HK1405715-007		**17**	**2**			
MP6-2	[24-FEB-2014]	HK1405715-008		**17**	<2			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3313272)								
HK1405689-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK1405715-002	MP3-2	EA025: Suspended Solids (SS)	----	2	mg/L	24	25	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3313272)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	102	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3312588)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	98.9	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1405953**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **26-FEB-2014**		
Order number	: **----**			*Date of issue*	: **06-MAR-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1405953 supersedes any previous reports with this reference. The completion date of analysis is 03-MAR-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1405953 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[26-FEB-2014]	HK1405953-001	**22**	**6**			
MP3-2	[26-FEB-2014]	HK1405953-002	**23**	**7**			
MP4-1	[26-FEB-2014]	HK1405953-003	**22**	**2**			
MP4-2	[26-FEB-2014]	HK1405953-004	**21**	**2**			
MP5-1	[26-FEB-2014]	HK1405953-005	**23**	<2			
MP5-2	[26-FEB-2014]	HK1405953-006	**22**	<2			
MP6-1	[26-FEB-2014]	HK1405953-007	**31**	<2			
MP6-2	[26-FEB-2014]	HK1405953-008	**28**	**2**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3315384)								
HK1405919-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK1405939-008	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	3	3	0.0
EA/ED: Physical and Aggregate Properties (QC Lot: 3315385)								
HK1405953-005	MP5-1	EA025: Suspended Solids (SS)	----	2	mg/L	23	23	0.0
HK1405954-007	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	4	4	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3315384)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	100	----	87	111	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 3315385)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	100	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3316764)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	91.8	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	: **ENOVATIVE ENVIRONMENTAL SERVICE LTD**	*Laboratory*	: **ALS Technichem HK Pty Ltd**	*Page*	: **1 of 3**		
Contact	: **MR THOMAS WONG**	*Contact*	: **Fung Lim Chee, Richard**	*Work Order*	: **HK1406221**		
Address	: **RM811, HIN PUI HOUSE, HIN KENG ESTATE, TAI WAI, N.T., HONG KONG**	*Address*	: **11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong**				
E-mail	: **Thomas.wong@eno.com.hk**	*E-mail*	: **Richard.Fung@alsglobal.com**				
Telephone	: **----**	*Telephone*	: **+852 2610 1044**				
Facsimile	: **----**	*Facsimile*	: **+852 2610 2021**				
Project	: **PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG**	*Quote number*	: **HK/1577/2009****	*Date received*	: **28-FEB-2014**		
Order number	: **----**			*Date of issue*	: **06-MAR-2014**		
C-O-C number	: **----**			*No. of samples*	- *Received* : **8**		
Site	: **----**				- *Analysed* : **8**		

Report Comments

This report for ALS Technichem (HK) Pty Ltd work order reference HK1406221 supersedes any previous reports with this reference. The completion date of analysis is 05-MAR-2014. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release. When date(s) and/or time(s) are shown bracketed, these have been assumed by the laboratory for process purposes. Abbreviations: CAS number = Chemical Abstract Services number. LOR = Limit of reporting.

Specific comments for Work Order HK1406221 : Sample(s) were received in a chilled condition.
Water sample(s) analysed and reported on an as received basis.

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

This document has been electronically signed by those names that appear on this report and are the authorised signatories. Electronic signing has been carried out in compliance with procedures specified in the 'Electronic Transactions Ordinance' of Hong Kong, Chapter 553, Section 6.

Signatory	*Position*	*Authorised results for:-*
Fung Lim Chee, Richard	**General Manager**	**Inorganics**

Analytical Results

Sub-Matrix: **WATER**

Compound			**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**			
LOR Unit			2 mg/L	2 mg/L			
Client sample ID	*Client sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics			
MP3-1	[28-FEB-2014]	HK1406221-001	**90**	**7**			
MP3-2	[28-FEB-2014]	HK1406221-002	**86**	**8**			
MP4-1	[28-FEB-2014]	HK1406221-003	**20**	**3**			
MP4-2	[28-FEB-2014]	HK1406221-004	**18**	**2**			
MP5-1	[28-FEB-2014]	HK1406221-005	**19**	**2**			
MP5-2	[28-FEB-2014]	HK1406221-006	**19**	**2**			
MP6-1	[28-FEB-2014]	HK1406221-007	**20**	**2**			
MP6-2	[28-FEB-2014]	HK1406221-008	**19**	**2**			

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Client sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 3321349)								
HK1406221-001	MP3-1	EA025: Suspended Solids (SS)	----	2	mg/L	90	93	3.5
HK1406237-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 3321349)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	102	----	87	111	----	----
EP: Aggregate Organics (QCLot: 3320938)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	95.6	----	78	112	----	----
EP: Aggregate Organics (QCLot: 3320939)											
EP030: Biochemical Oxygen Demand	----	2	mg/L	----	198 mg/L	91.4	----	78	112	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

Appendix G. Weather Conditions during the Monitoring Period

Wind Data for Wetland Park

11 February 2014

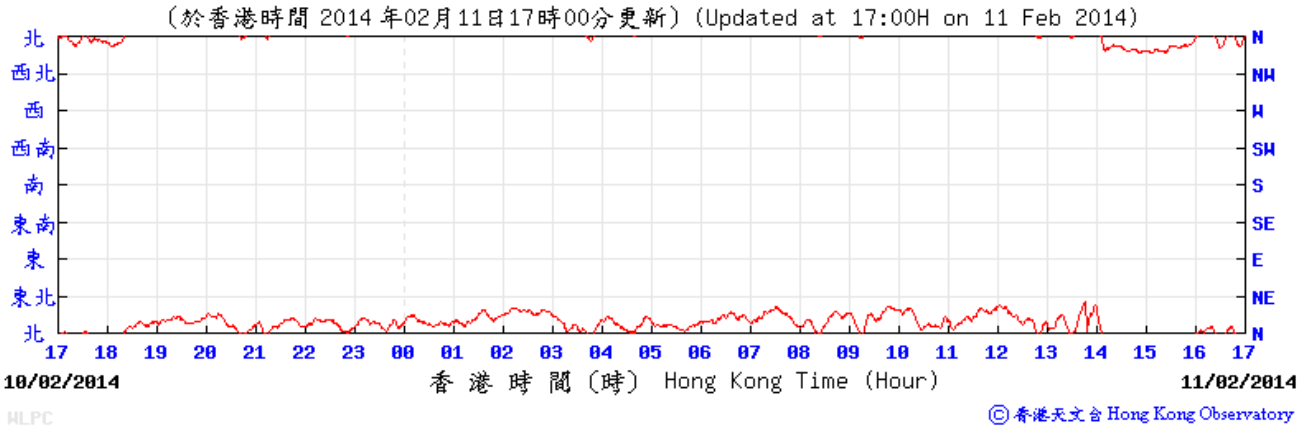

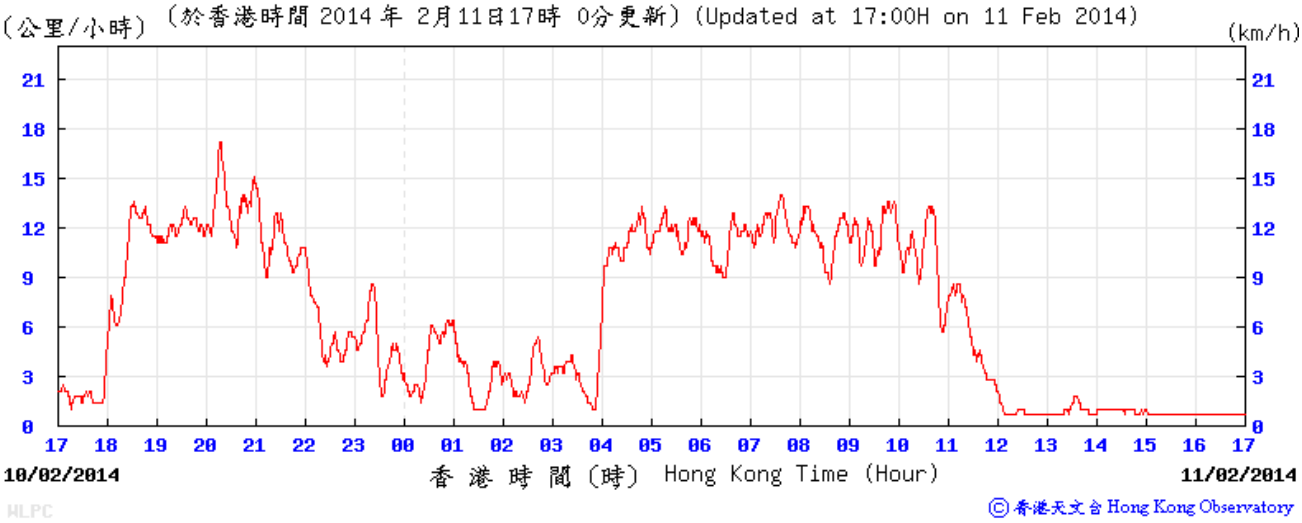



Wind Data for Wetland Park

12 February 2014

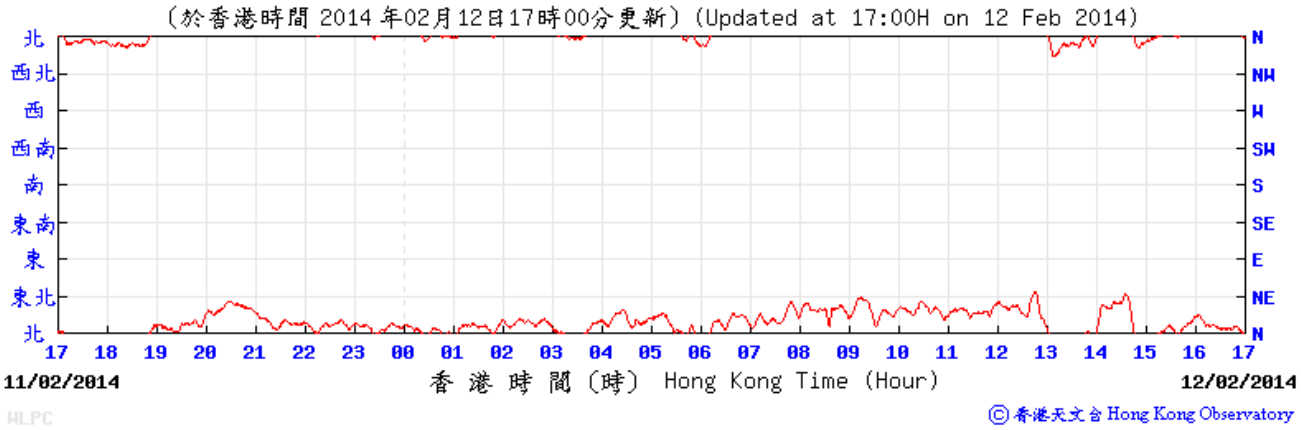

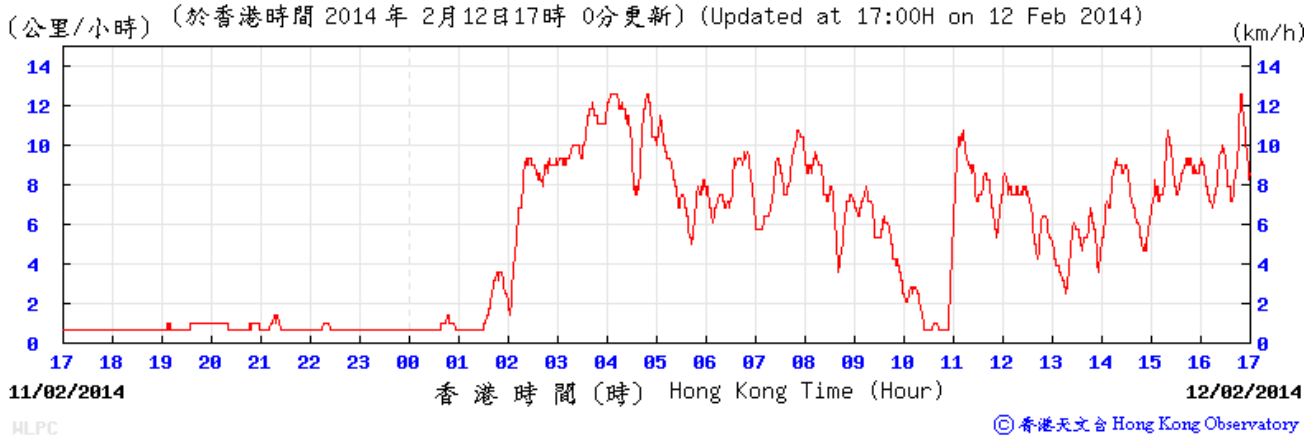



Wind Data for Wetland Park

17 February 2014

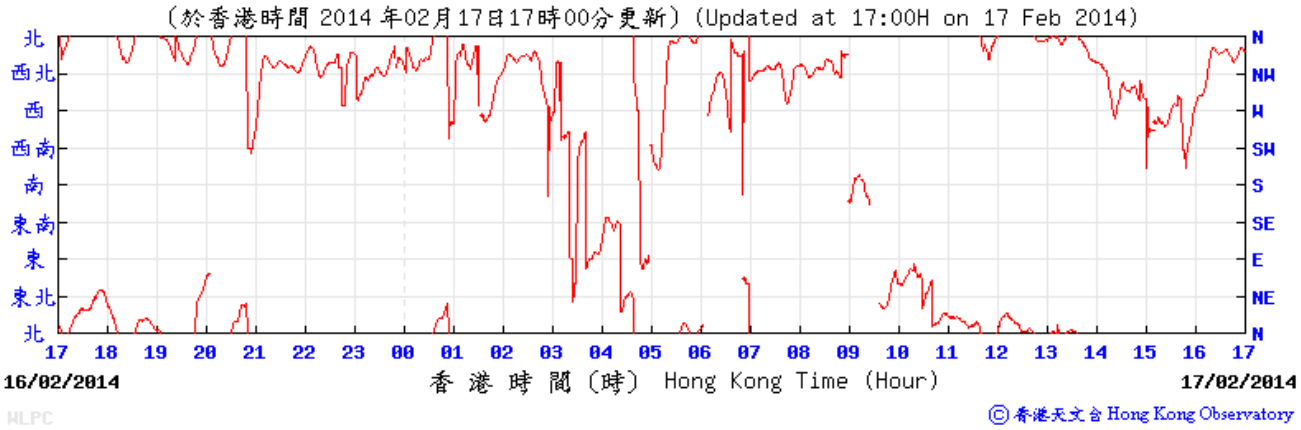

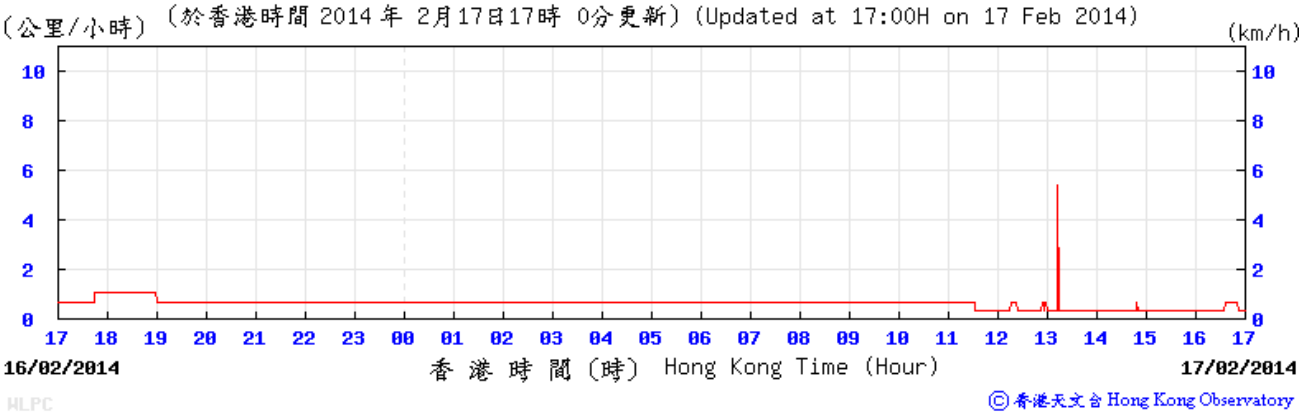



Wind Data for Wetland Park

18 February 2014

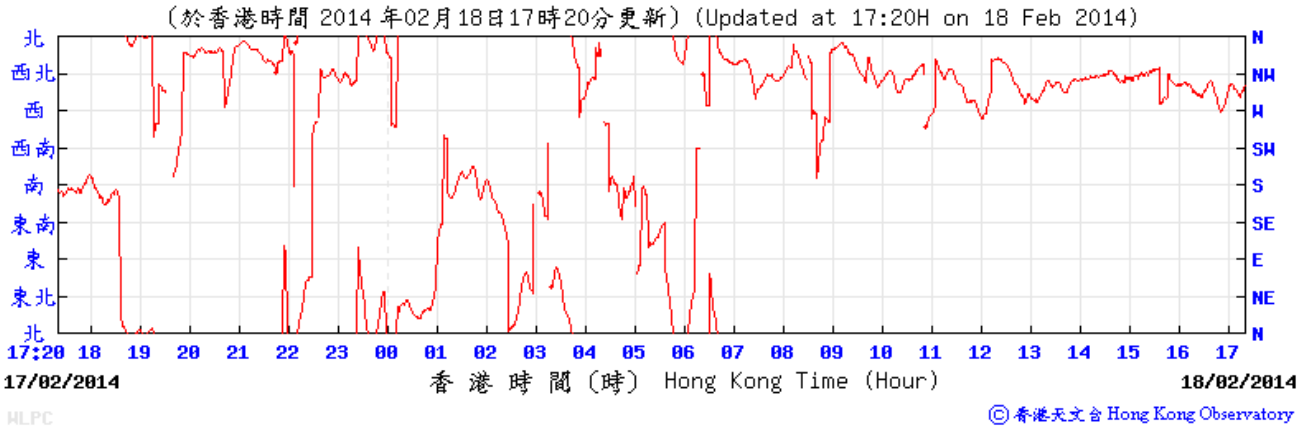

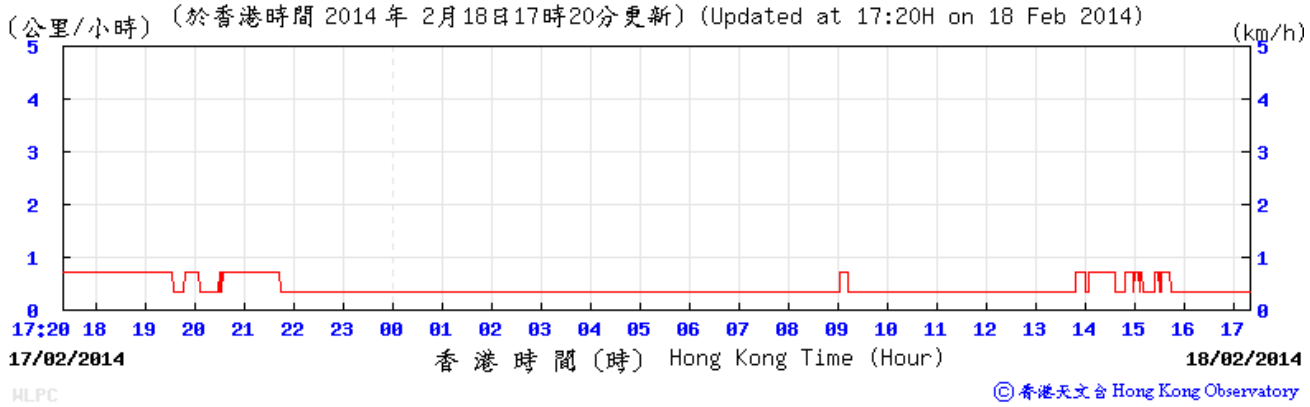



Wind Data for Wetland Park

21 February 2014

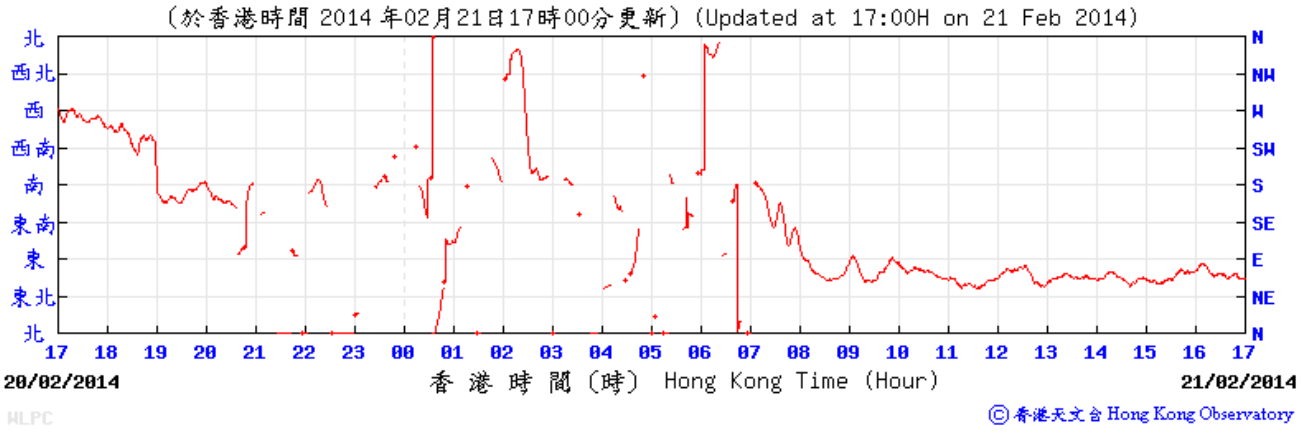

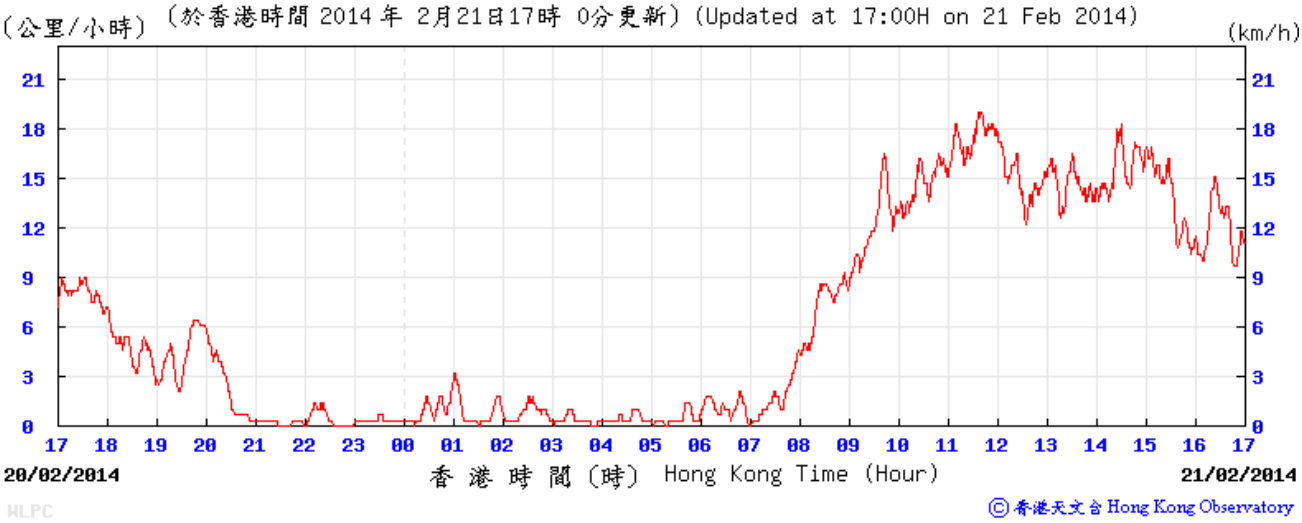



Wind Data for Wetland Park

22 February 2014

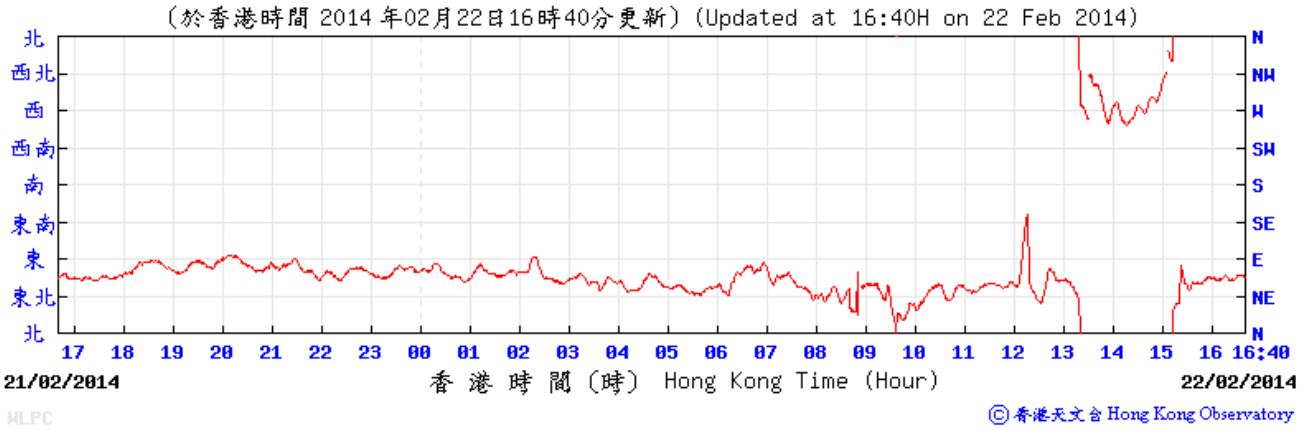

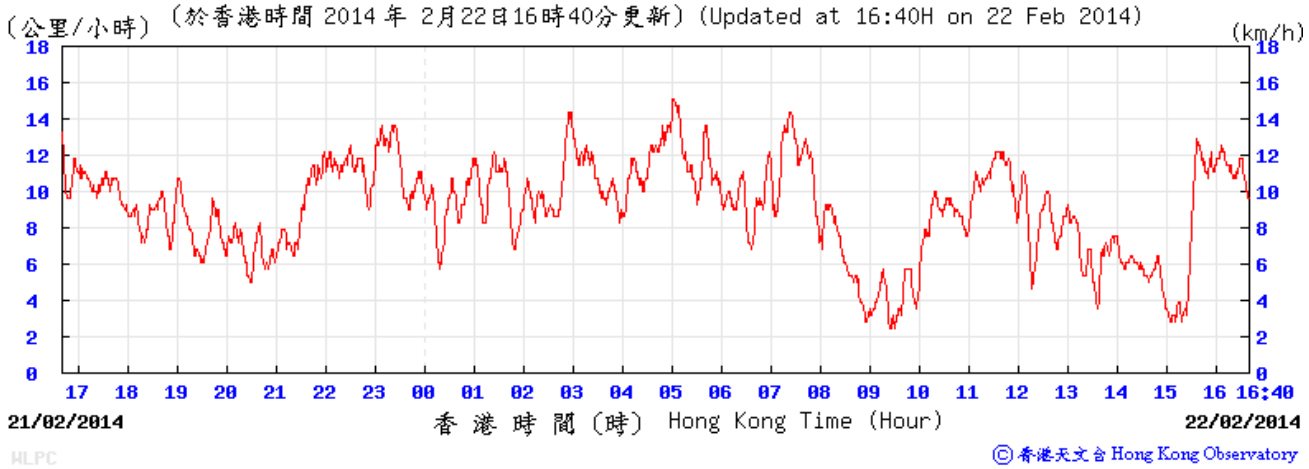



Wind Data for Wetland Park

27 February 2014

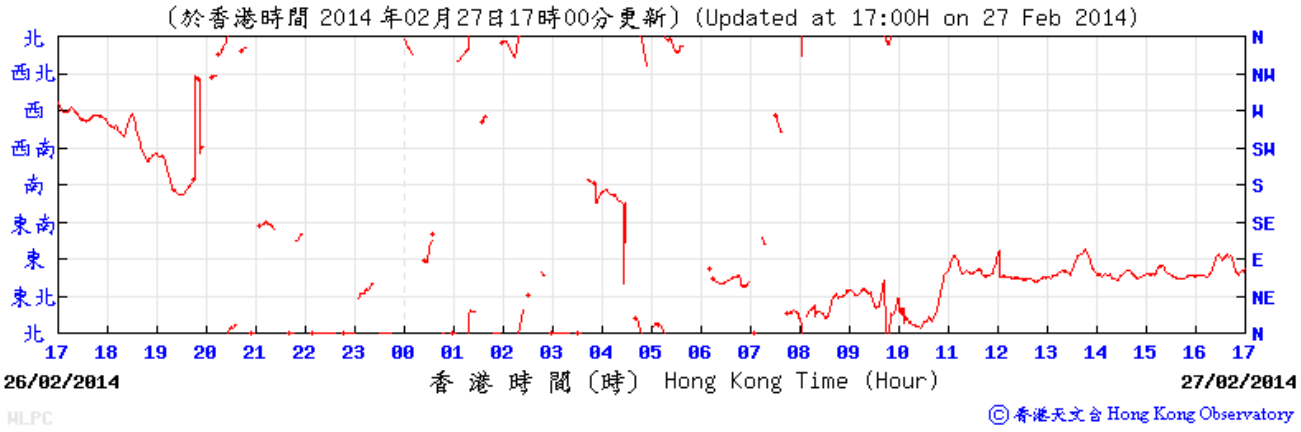

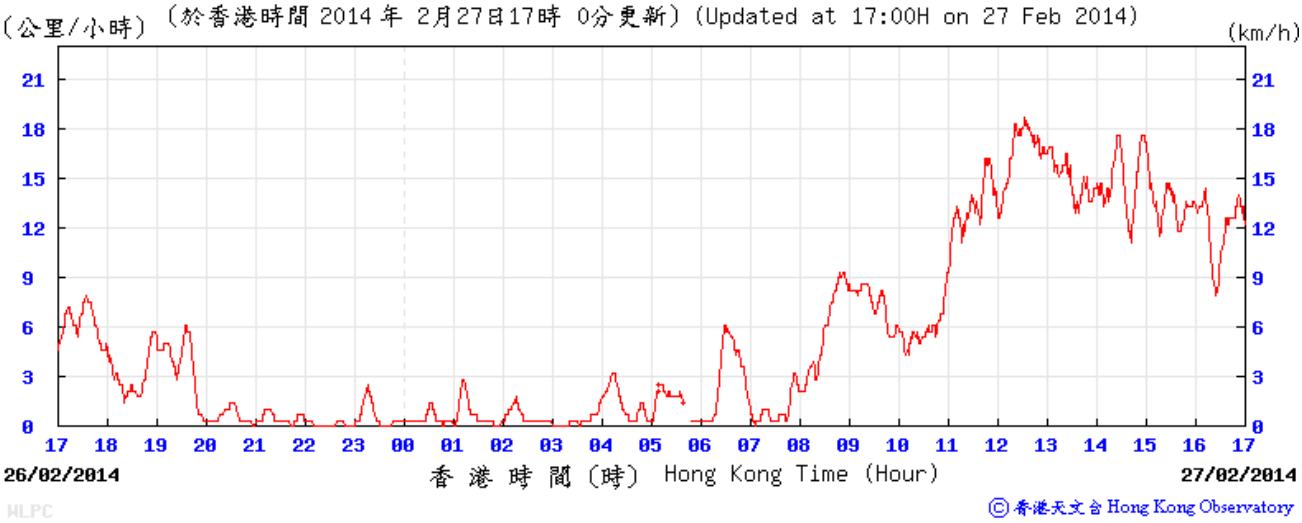



Wind Data for Wetland Park

28 February 2014

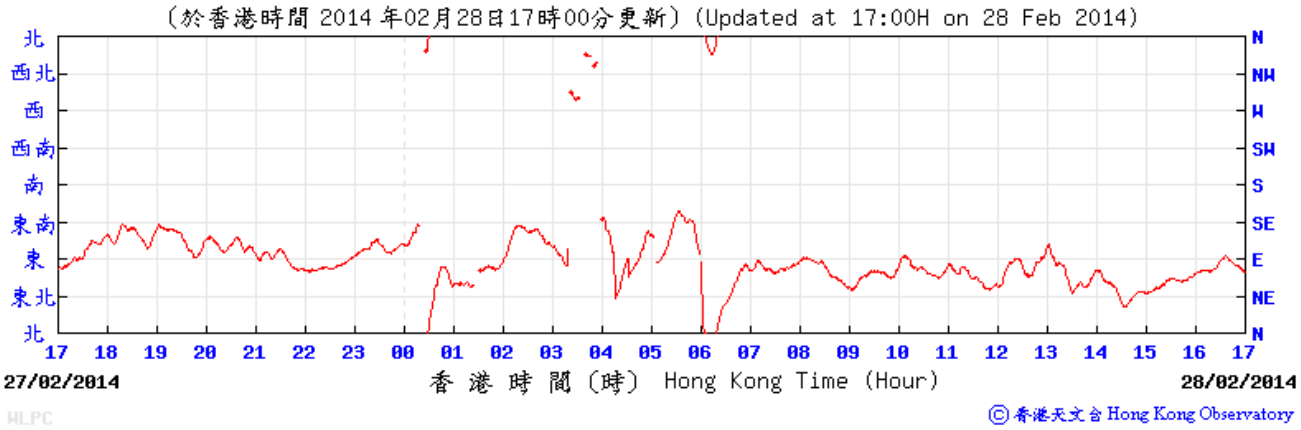

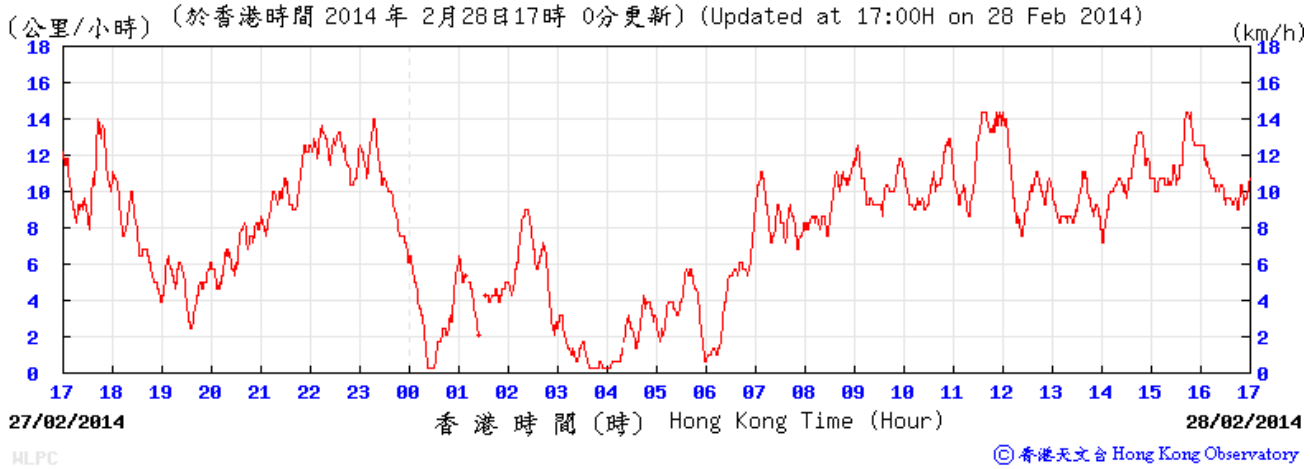



Wind Data for Lau Fau Shan

11 February 2014

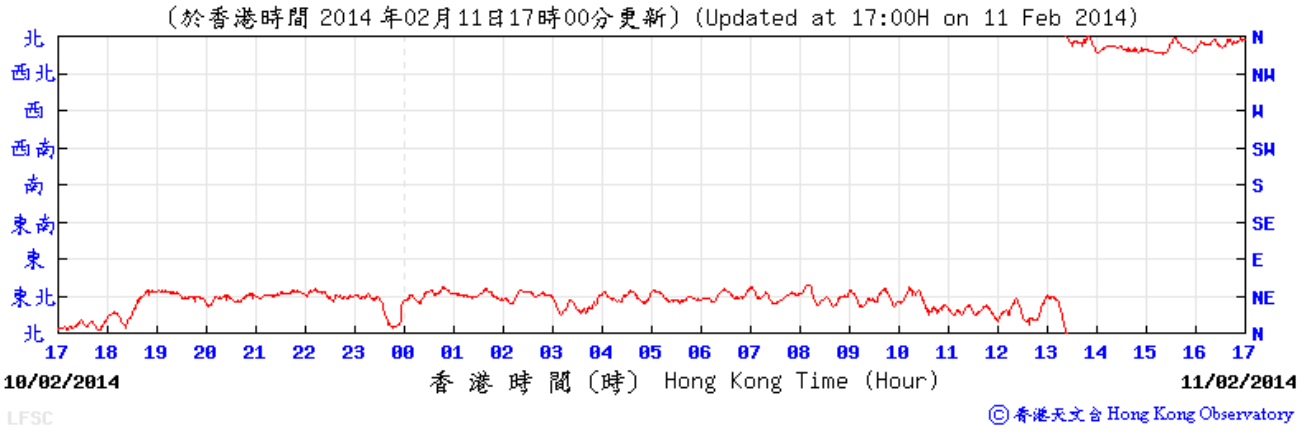

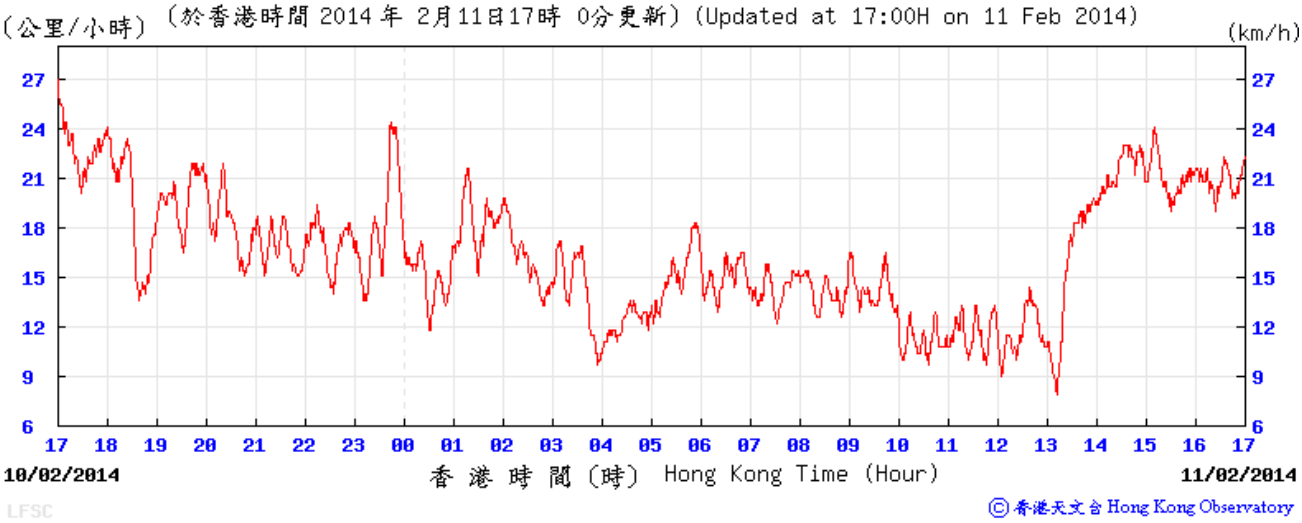



Wind Data for Lau Fau Shan

12 February 2014

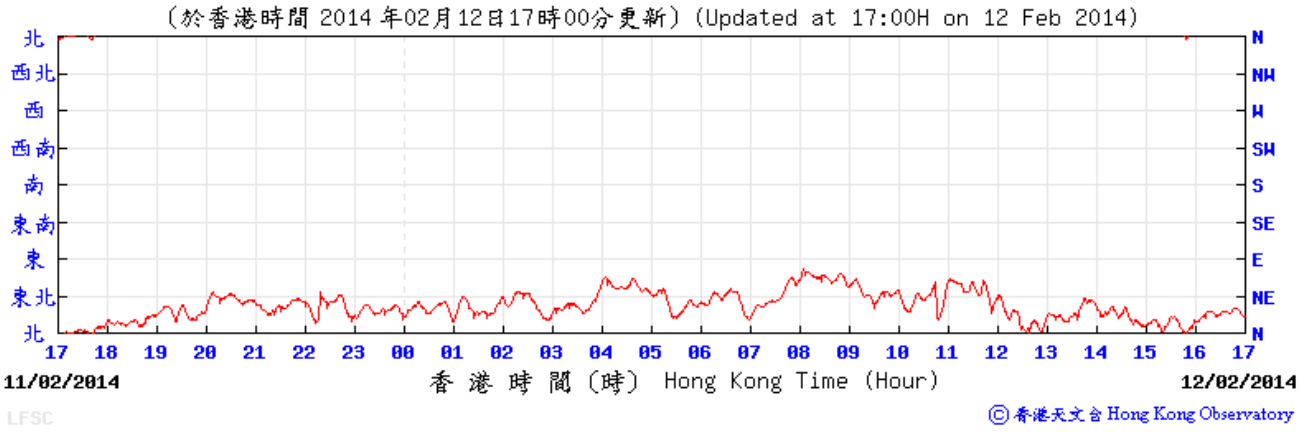

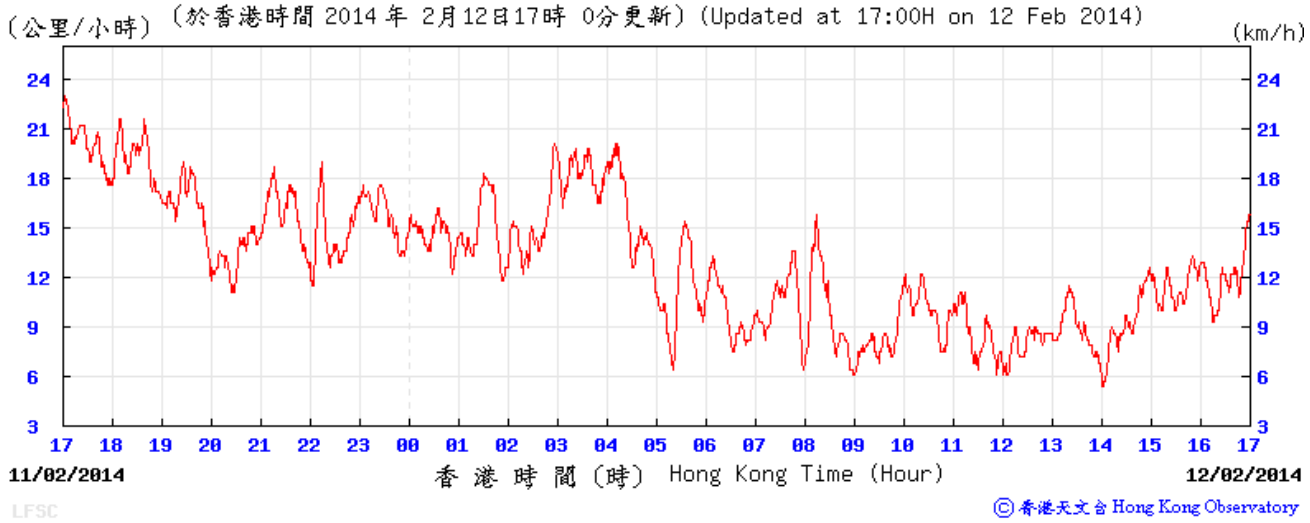



Wind Data for Lau Fau Shan

17 February 2014

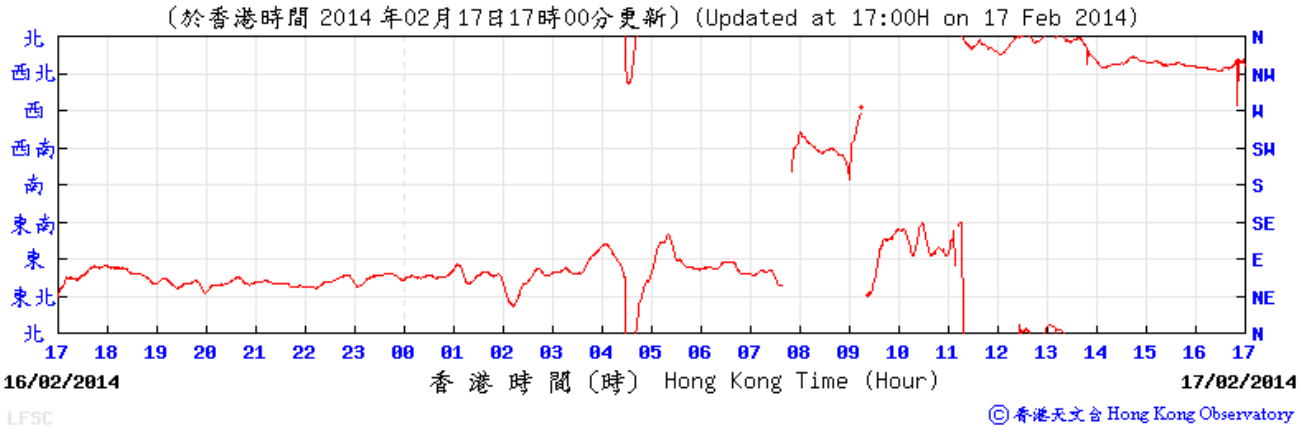

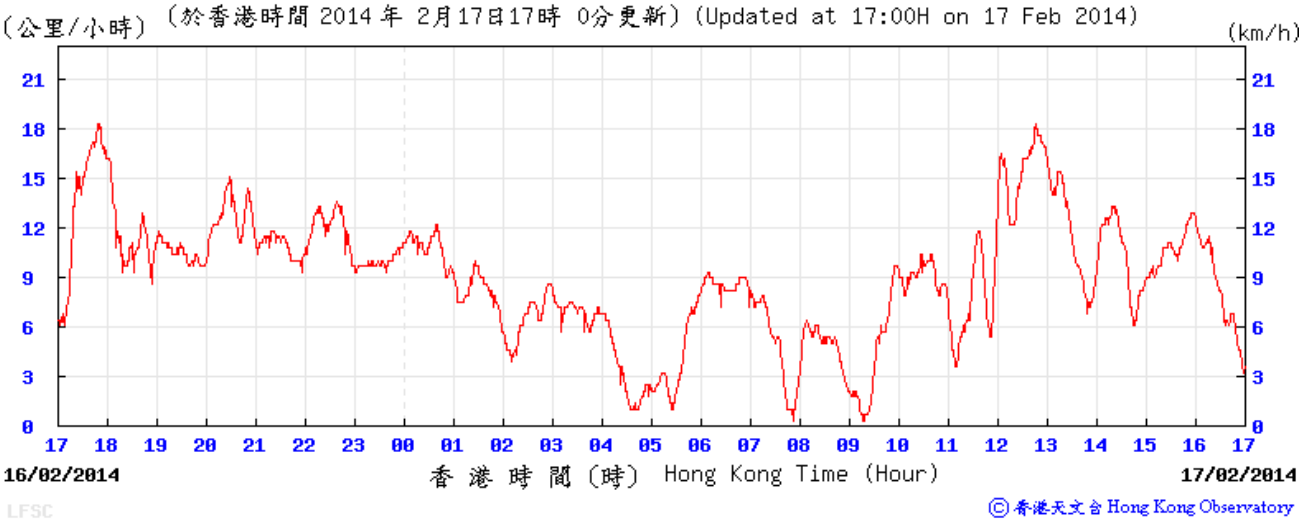



Wind Data for Lau Fau Shan

18 February 2014

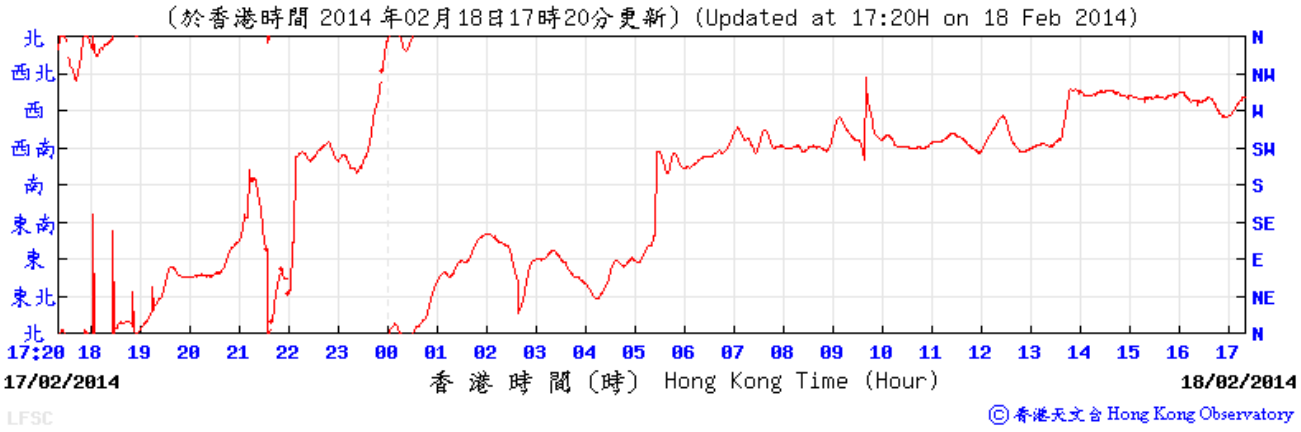

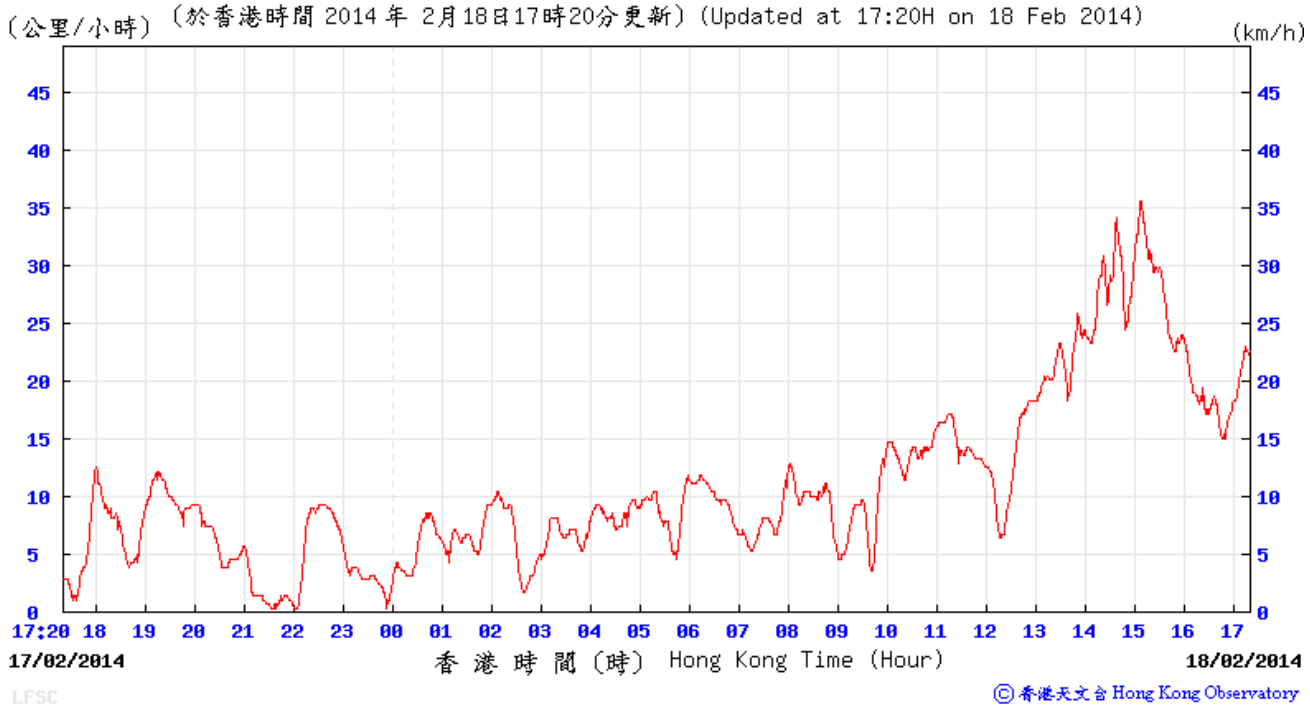



Wind Data for Lau Fau Shan

21 February 2014

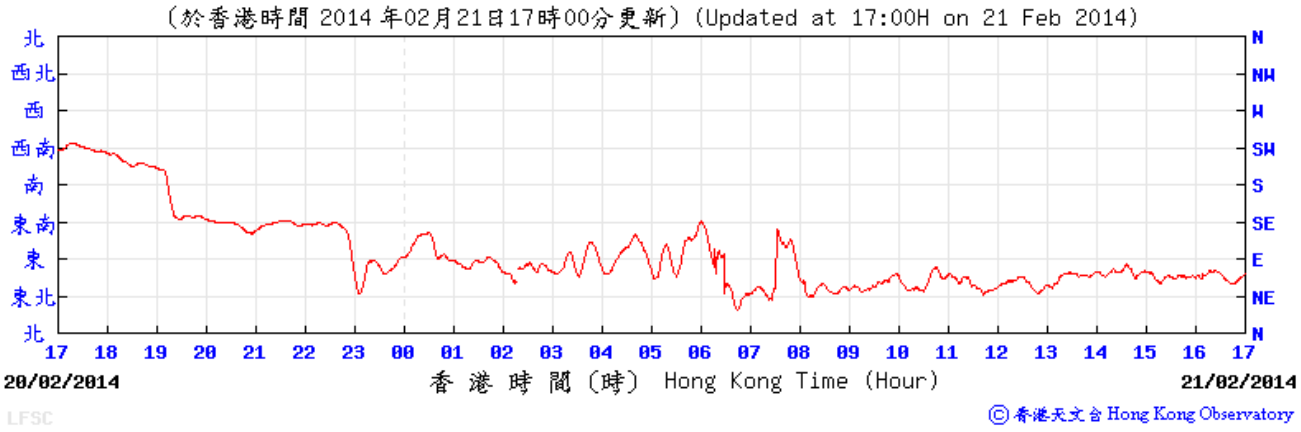

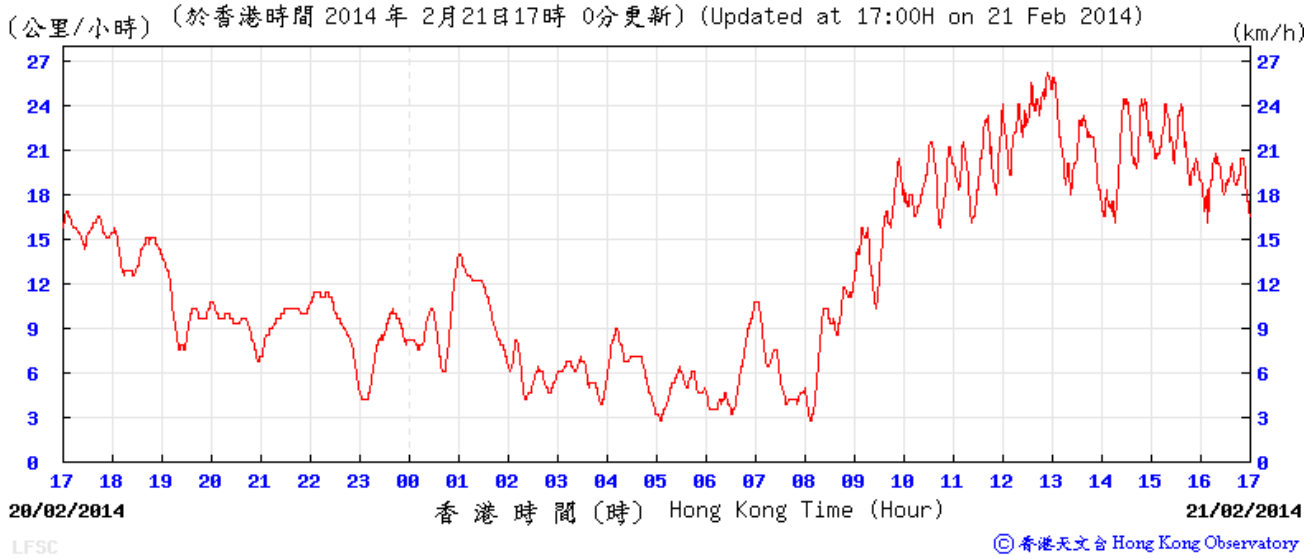



Wind Data for Lau Fau Shan

22 February 2014

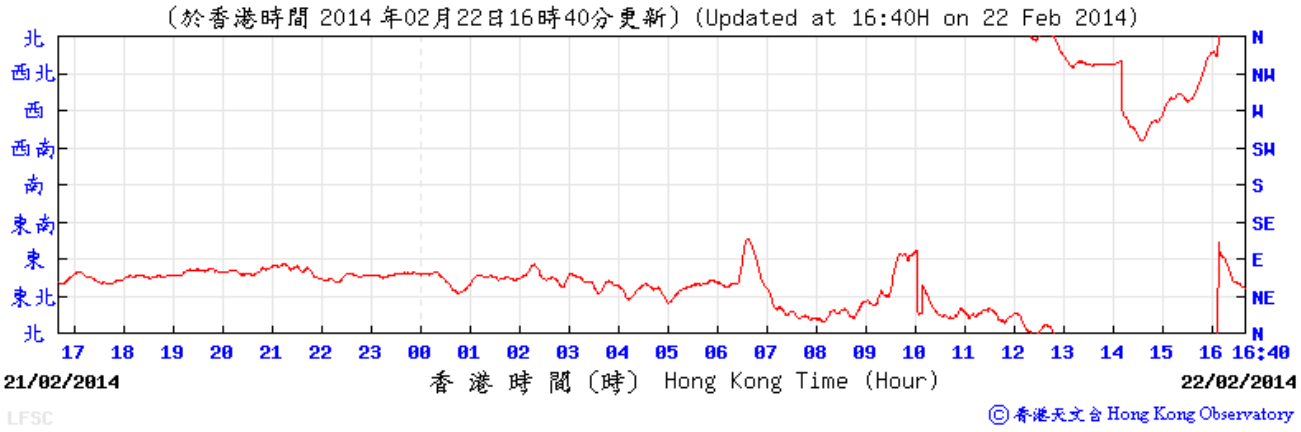

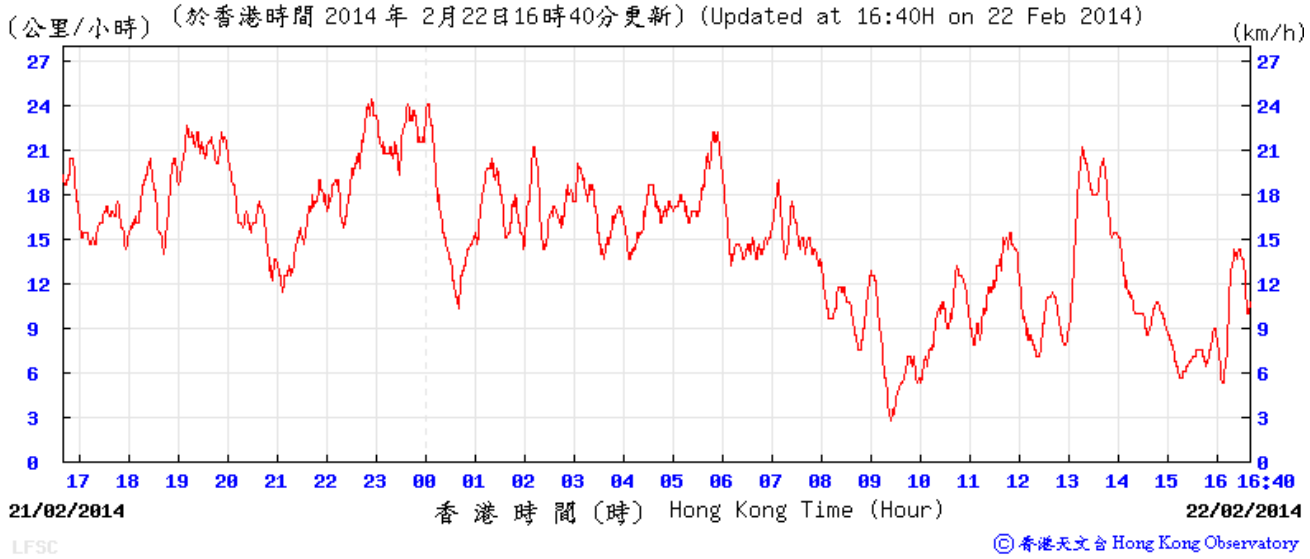



Wind Data for Lau Fau Shan

27 February 2014

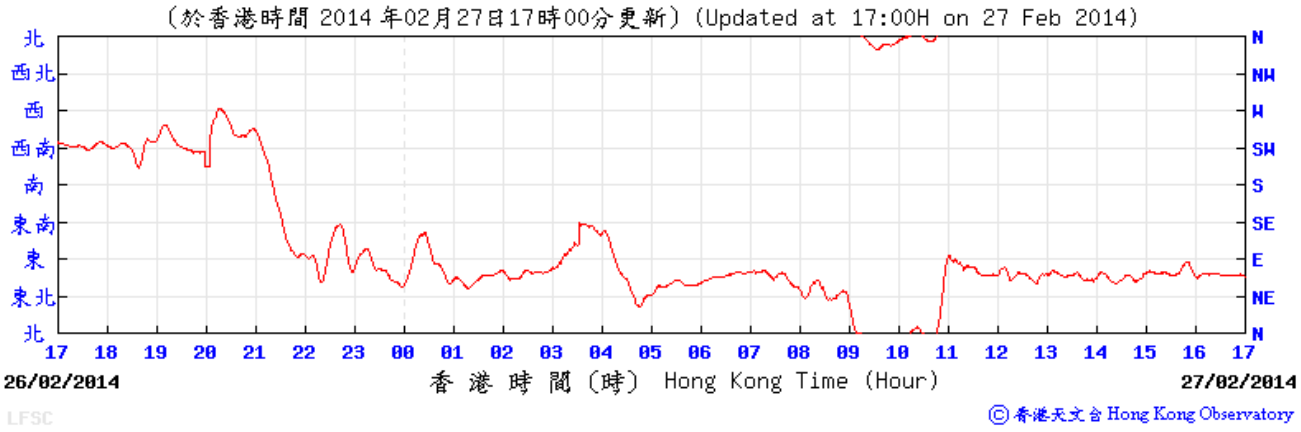

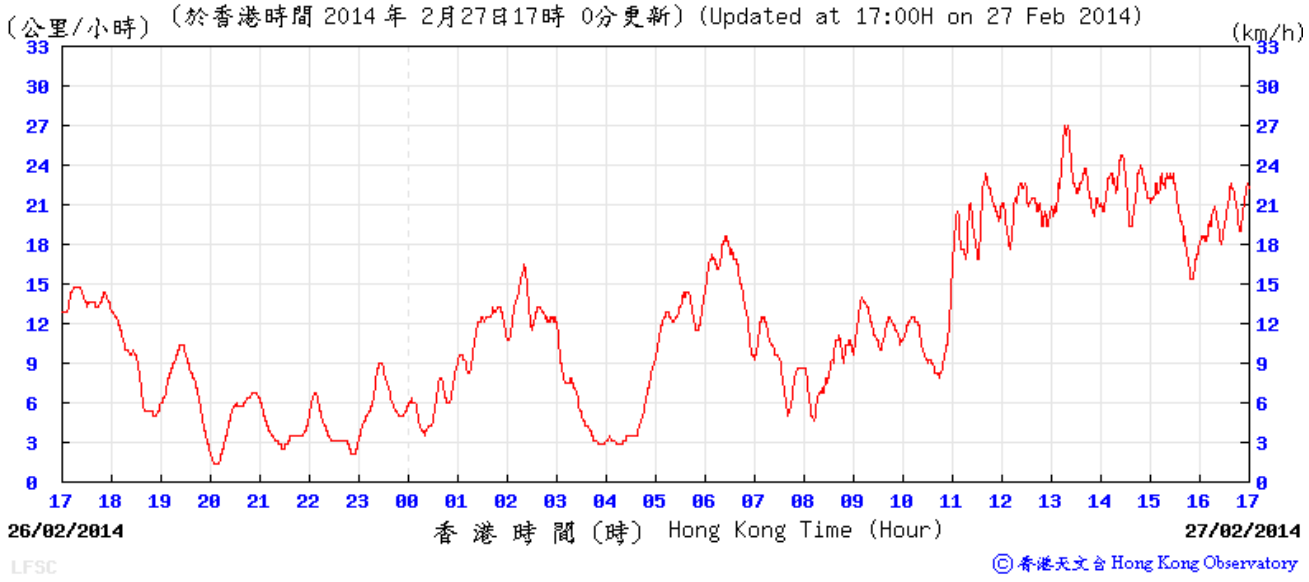



Wind Data for Lau Fau Shan

28 February 2014

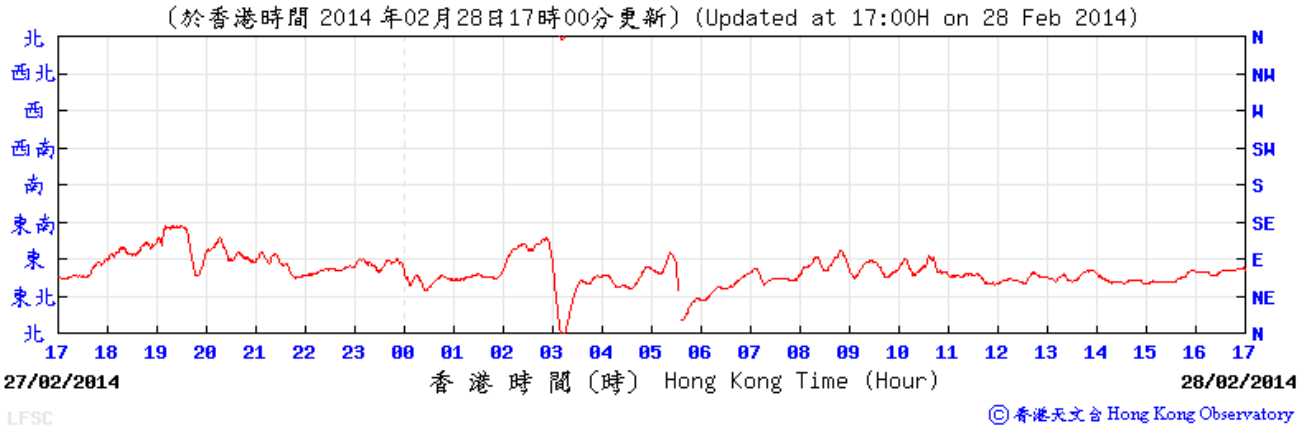

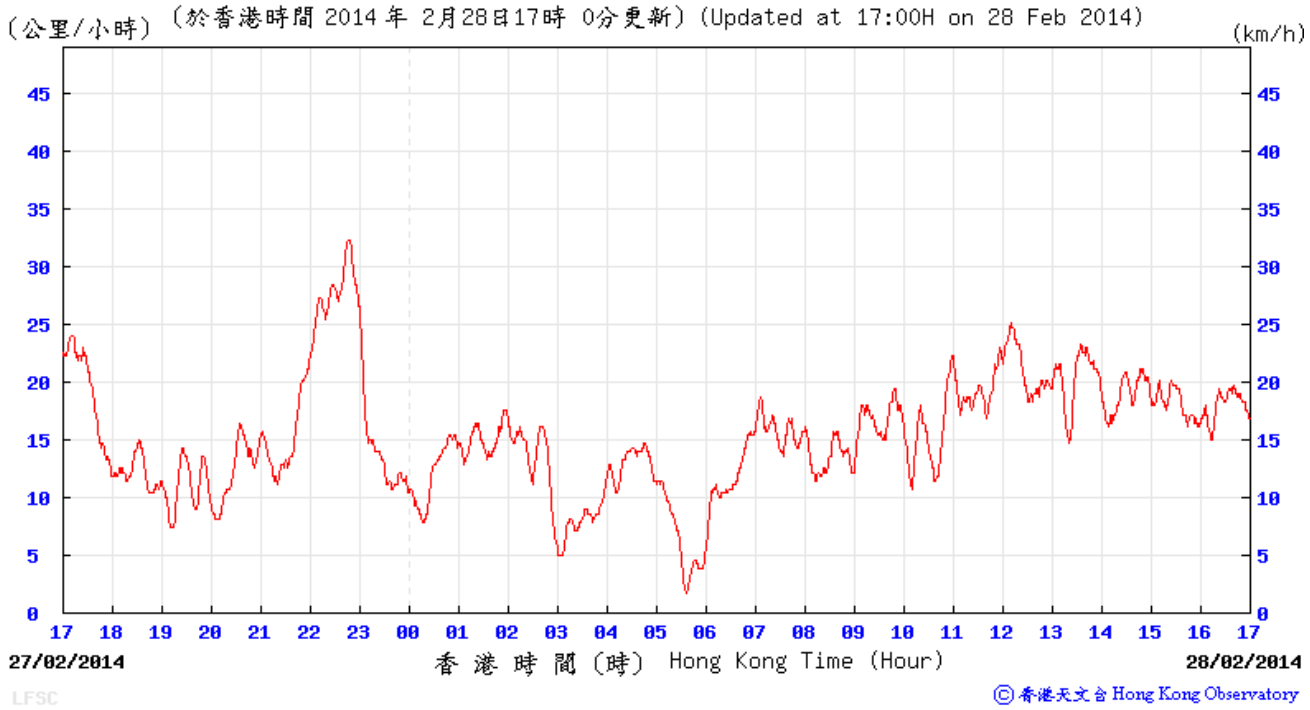



EXTRACT OF METEOROLOGICAL OBSERVATIONS FOR HONG KONG, FEBRUARY 2014 (Table 1)

Date FEBRUARY	Mean Pressure (hPa)	Air Temperature			Mean Dew Point Temperature (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)				
1	1015.4	22.2	20.0	18.3	17.0	83	34	-
2	1011.6	23.8	20.2	17.5	15.4	76	16	-
3	1010.0	24.6	20.6	17.4	14.9	71	3	-
4	1013.3	19.4	18.2	16.6	15.1	82	73	Trace
5	1013.9	19.0	17.1	15.9	14.1	82	82	Trace
6	1012.1	21.6	18.6	16.7	16.3	87	81	Trace
7	1010.9	23.4	20.3	18.1	18.0	87	84	Trace
8	1011.4	18.0	16.6	16.0	14.9	90	88	0.3
9	1012.3	16.7	14.5	10.4	13.7	95	93	13.1
10	1019.1	10.5	9.1	8.3	5.3	77	88	0.3
11	1019.9	9.7	8.4	7.5	3.1	69	89	Trace
12	1018.8	10.5	8.9	7.3	6.6	85	96	0.4
13	1021.3	9.8	8.7	8.0	7.2	91	96	21.4
14	1022.1	14.6	10.6	8.2	4.8	67	64	-
15	1020.4	13.6	11.8	9.7	8.1	79	86	Trace
16	1018.6	15.4	14.2	13.3	12.5	89	100	Trace
17	1018.1	20.9	17.6	15.3	16.6	95	90	-
18	1016.4	21.5	17.0	12.2	15.3	90	88	Trace
19	1021.5	12.4	10.0	7.9	5.6	75	84	3.8
20	1024.8	17.3	12.3	8.2	4.8	62	5	-
21	1024.5	15.2	13.8	12.3	9.3	75	74	-
22	1023.0	17.1	14.7	12.6	10.5	77	85	0.2
23	1022.7	19.2	16.2	14.4	12.4	78	52	-
24	1020.6	19.3	17.0	15.0	14.0	82	64	Trace
25	1018.6	20.9	18.7	17.3	16.0	85	83	-
26	1018.0	24.1	20.2	17.9	17.9	87	73	Trace
27	1018.9	21.1	19.6	18.7	17.7	89	80	Trace
28	1017.0	19.0	18.3	17.4	16.1	87	88	Trace
Mean/Total	1017.7	17.9	15.5	13.5	12.3	82	73	39.5
Normal*	1018.5	18.9	16.8	15.0	13.0	80	74	54.4
Station	Hong Kong Observatory							

EXTRACT OF METEOROLOGICAL OBSERVATIONS FOR HONG KONG, FEBRUARY 2014 (Table 2)

Date FEBRUARY	Number of hours of Reduced Visibility# (hours)	Total Bright Sunshine (hours)	Daily Global Solar Radiation (MJ/m^2)	Total Evaporation (mm)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
1	3	6.5	11.60	2.9	050	10.8
2	4	9.7	18.31	2.8	020	10.0
3	0	10.2	18.68	3.5	280	9.4
4	2	0.4	5.17	2.1	100	40.3
5	0	3.2	12.51	2.4	080	35.6
6	0	5.1	14.55	2.4	050	16.0
7	0	3.2	11.85	2.0	050	10.5
8	0	-	1.78	0.3	040	22.5
9	0	-	1.11	1.5	030	36.7
10	3	-	3.49	1.9	030	39.2
11	0	-	4.38	1.4	030	28.1
12	6	-	2.36	0.3	030	24.2
13	2	-	3.03	1.2	020	30.2
14	9	4.9	13.65	2.8	030	25.3
15	0	-	3.30	0.4	060	32.2
16	13	-	4.70	0.8	060	33.0
17	7	4.2	12.91	1.6	050	18.5
18	0	0.9	8.03	2.8	020	16.3
19	0	0.1	4.24	2.6	020	39.7
20	0	10.7	22.99	3.3	070	22.1
21	0	3.9	15.11	3.3	080	41.2
22	0	2.6	11.90	3.1	070	40.3
23	0	9.6	20.52	3.3	070	34.6
24	0	6.3	17.24	3.2	070	34.8
25	2	4.2	13.40	2.0	050	24.7
26	6	5.2	13.65	2.6	050	13.5
27	0	1.0	7.18	2.3	050	25.8
28	1	-	4.72	1.0	060	28.7
Mean/Total	58	91.9	10.08	59.8	050	26.6
Normal*	139.2§	94.2	9.39	59.9	070	24.5
Station	Hong Kong International Airport	King's Park			Waglan Island	

The minimum pressure recorded at the Hong Kong Observatory was 1007.8 hectopascals at 1445 HKT on 3 February.

The maximum air temperature recorded at the Hong Kong Observatory was 24.6 degrees C at 1549 HKT on 3 February.

The minimum air temperature recorded at the Hong Kong Observatory was 7.3 degrees C at 0705 HKT on 12 February.

The maximum gust peak speed recorded at Waglan Island was 65 kilometres per hour from 030 degrees at 0604 HKT on 19 February.

The maximum instantaneous rate of rainfall recorded at King's Park was 62 millimetres per hour at 0858 HKT on 13 February.

Reduced visibility refers to visibility below 8 kilometres when there is no fog, mist, or precipitation.

-The visibility readings at the Hong Kong International Airport are based on hourly observations by professional meteorological observers in 2004 and before, and average readings over the 10-minute period before the clock hour of the visibility meter near the middle of the south runway from 2005 onwards. The change of the data source in 2005 is an improvement of the visibility assessment using instrumented observations following the international trend.

-Before 10 October 2007, the number of hours of reduced visibility at the Hong Kong International Airport in 2005 and thereafter displayed in this web page was based on hourly visibility observations by professional meteorological observers. Since 10 October 2007, the data have been revised using the average visibility readings over the 10- minute period before the clock hour, as recorded by the visibility meter near the middle of the south runway.

* 1981 - 2010 Climatological Normal, unless otherwise specified

§ 1997-2013 Mean value

Appendix H. Ecological Monitoring Conducted

February 2014	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
Mammals				✓							✓				
Birds				✓							✓				
Herpetofauna															
Dragonflies & butterflies															
Water Quality															
Inspection Visits				✓							✓			✓	

February 2014	16	17	18	19	20	21	22	23	24	25	26	27	28
Mammals			✓							✓			
Birds			✓							✓			
Herpetofauna													
Dragonflies & butterflies													
Water Quality						✓							✓
Inspection Visits			✓			✓				✓			

Note: Light grey cells indicate public holidays, Saturdays or Sundays. Black cells indicate survey item not required in the reporting month

.

Appendix I. Summary of Bird Surveys Conducted

Table I1. Summary of bird species of conservation importance and/or wetland-dependence recorded in the Survey Area (excluding the WRA)

Species Name[5]	*Scientific Name*[5]	Conservation Status [2]	February 2014		Records outside surveys
			Occurrence[3]	Mean[4]	
Little Grebe	*Tachybaptus ruficollis*	LC, (1)	4	6.3	✓
Great Cormorant	*Phalacrocorax carbo*	PRC, (1)	4	5.3	✓
Grey Heron	*Ardea cinerea*	PRC, (1)	4	3.0	✓
Great Egret	*Egretta alba*	PRC, (RC), (1)	3	3.0	✓
Little Egret	*Egretta garzetta*	PRC, (RC), (1)	4	13.5	✓
Chinese Pond Heron	*Ardeola bacchus*	PRC, (RC), (1)	4	6.8	✓
Black-faced Spoonbill	*Platalea minor*	PGC, (1)	2	2.0	✓
Tufted Duck	*Aythya fuligula*	LC, (1)	4	18.3	✓
Black Kite	*Milvus migrans*	RC, (1)	1	0.5	✓
White-breasted Waterhen	*Amaurornis phoenicurus*	(1)	1	0.5	✓
Common Moorhen	*Gallinula chloropus*	(1)	1	0.5	✓
Little Ringed Plover	*Charadrius dubius*	(LC), (1)	2	1.0	✓
Common Sandpiper	*Actitis hypoleucos*	(1)	4	3.5	✓
Whiskered Tern	*Chlidonias hybrida*	LC, (1)	1	0.8	✓
Pied Kingfisher	*Ceryle rudis*	(LC), (1)	1	0.3	✓
White-throated Kingfisher	*Halcyon smyrnensis*	LC, (1)	2	0.5	
Common Kingfisher	*Alcedo atthis*	(1)	2	0.5	✓
Eastern Yellow Wagtail	*Motacilla tschutschensis*	(1)	4	2.0	✓
White Wagtail	*Motacilla alba*	(1)	4	11.8	✓
Richard's Pipit	*Anthus richardi*	(1)	2	0.8	✓
Red-billed Starling	*Spodiopsar sericeus*	(1)	2	6.8	✓
No. of Species Recorded				**21**	

(1) Indicates wetland-dependant or wetland-associated species.
(2) Conservation status follows that of Fellowes *et al.* (2002) and BirdLife International listing (2011).
(3) Indicates number of surveys recorded within the reporting period.
(4) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA)
(5) Follows HK bird list (dated 2013-2-25).

Table I2. Summary of bird species of conservation importance and/or wetland-dependence recorded in the WRA

Species Name[5]	*Scientific Name*[5]	Conservation Status [2]	February 2014		Records outside surveys
			Occurrence[3]	Mean[4]	
Little Grebe	*Tachybaptus ruficollis*	LC, (1)	4	5.3	✓
Great Cormorant	*Phalacrocorax carbo*	PRC, (1)	1	0.5	
Grey Heron	*Ardea cinerea*	PRC, (1)	3	2.5	✓
Great Egret	*Egretta alba*	PRC, (RC), (1)	3	1.8	✓
Intermediate Egret	*Egretta intermedia*	RC, (1)	-	-	✓
Little Egret	*Egretta garzetta*	PRC, (RC), (1)	4	4.0	✓
Chinese Pond Heron	*Ardeola bacchus*	PRC, (RC), (1)	4	3.5	✓

Species Name[5]	*Scientific Name*[5]	Conservation Status [2]	February 2014		Records outside surveys
			Occurrence[3]	Mean[4]	
Black-faced Spoonbill	*Platalea minor*	PGC, (1)	-	-	✓
Northern Shoveler	*Anas clypeata*	RC, (1)	2	5.5	✓
Black Kite	*Milvus migrans*	RC, (1)	2	0.5	✓
Crested Serpent Eagle	*Spilornis cheela*	(LC), (1)	-	-	✓
Little Ringed Plover	*Charadrius dubius*	(LC), (1)	1	0.5	✓
Wood Sandpiper	*Tringa glareola*	(LC), (1)	-	-	✓
Common Sandpiper	*Actitis hypoleucos*	(1)	1	0.3	✓
Eurasian Eagle Owl	*Bubo bubo*	RC	-	-	✓
Pied Kingfisher	*Ceryle rudis*	(LC), (1)	1	0.3	✓
Common Kingfisher	*Alcedo atthis*	(1)	4	2.3	✓
Eastern Yellow Wagtail	*Motacilla tschutschensis*	(1)	3	1.0	✓
White Wagtail	*Motacilla alba*	(1)	4	1.3	✓
Richard's Pipit	*Anthus richardi*	(1)	4	2.0	✓
Chinese Penduline Tit	*Remiz consobrinus*	RC, (1)	1	4.5	✓
Red-billed Starling	*Spodiopsar sericeus*	(1)	-	-	✓
Collared Crow	*Corvus torquatus*	LC, (1)	-	-	✓
No. of Species Recorded				**23**	

(1) Indicates wetland-dependant or wetland-associated species.
(2) Conservation status follows that of Fellowes *et al.* (2002) and BirdLife International listing (2011).
(3) Indicates number of surveys recorded within the reporting period.
(4) Refers to the mean number of individuals recorded in the reporting period at WRA.
(5) Follows HK bird list (dated 2013-02-25).
(*) Eurasian Eagle Owl was observed at the boundary between the Wetland Restoration Area and the construction site of Wo Shang Wai.

Appendix J. Summary of Herpetofauna, Mammal and Insect Surveys Conducted

Table J1. Summary of herpetofauna monitoring in the Survey Area (excluding the WRA)

Species Name	Scientific Name	Conservation Status[1]	Feb 2014	
			Occurrence[2]	Mean[3]
Amphibian	**No. of Species Recorded**		**0**	
(No Records in February 2014)				
			Occurrence[2]	**Mean[3]**
Reptile	**No. of Species Recorded**		**0**	
(No Records in February 2014)				

(1) Conservation status follows that of Fellowes *et al.* (2002), Chan *et al.* (2005) and Karsen *et al.* (1998).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA).

Table J2. Summary of herpetofauna monitoring in the WRA

Species Name	Scientific Name	Conservation Status[1]	Feb 2014		Records Outside Surveys
			Occurrence[2]	Mean[3]	
Amphibian	**No. of Species Recorded**				
(No Records in February 2014)					
			Occurrence[2]	**Mean[3]**	
Reptiles	**No. of Species Recorded**				
(No Records in February 2014)					

(1) Conservation status follows that of Fellowes *et al.* (2002), Chan *et al.* (2005) and Karsen *et al.* (1998).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period in the WRA.

Table J3. Summary of mammal monitoring in the Survey Area (excluding the WRA)

Species Name	Scientific Name	Conservation Status[1]	Feb 2014	
			Occurrence[2]	Mean[3]
Mammal	**No. of Species Recorded**		**0**	
(No Records in February 2014)				

(1) Conservation status follows that of Fellowes *et al.* (2002) and Shek (2006).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA).

Table J4. Summary of mammal monitoring in the WRA

Species Name	Scientific Name	Conservation Status[1]	Feb 2014		Records Outside Surveys
			Occurrence[2]	Mean[3]	
Mammal	**No. of Species Recorded**		**0**		
(No Records in February 2014)					

(1) Conservation status follows that of Fellowes *et al.* (2002) and Shek (2006).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period in the WRA.

Table J5. Summary of dragonflies (odonata) and butterfly monitoring in the Survey Area (excluding WRA)

Common Name	Scientific Name	Conservation Status[1]	Feb 2014	
			Occurrence[2]	Mean[3]
Odonata				
(No Records in February 2014)				
(No Records in February 2014)				

(1) Conservation status follows that of Fellowes *et al.* (2002), Lo & Hui (2004), Tam *et al.* (2011) and Young & Yiu (2002).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the survey (excluding the WRA).

Table J6. Summary of dragonfly and butterfly monitoring in the WRA

Common Name	Scientific Name	Conservation Status[1]	Feb 2014	
			Occurrence[2]	Mean[3]
Odonate	**No. of Species Recorded**		**0**	
(No Records in February 2014)				
Butterfly	**No. of Species Recorded**		**0**	
(No Records in February 2014)				

(1) Conservation status follows that of Fellowes *et al.* (2002), Lo & Hui (2004), Tam *et al.* (2011) and Young & Yiu (2002).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period in the WRA.

Appendix K. Summary of Monitoring of Water Quality associated with Ecological Monitoring Conducted

Table K1. Water quality at WRA in February 2014

Cell No.	Temp. (°C)	pH	Salinity (ppt)	Turb (mg/L)	DO (mg/L)	Water Level (cm)
1	14.8	7.93	0.51	26.6	12.4	160
2	14.9	7.82	0.65	22.1	11.4	**140**
3	15.4	7.76	0.63	21.3	10.6	180
4	15.6	7.84	0.64	26.6	10.6	180

Note: Values highlighted in bold indicate that action level is reached; whereas values in bold and underline indicate that limit level is reached.

Appendix L. Environmental Mitigation Measures - Implementation Status

Air Quality – Recommended Mitigation Measures

Air Quality Mitigation Measures during construction	Implementation Status
• access roads should be sprayed with water or dust suppression chemical to maintain the entire road surface wet or paved;	✓
• every stock of more than 20 bags of cement or dry PFA shold be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;	N/A
• de-bagging, batching or mixing process should be carried out in sheltered areas during the use of bagged cement;	N/A
• use of effective dust screens, sheeting or netting to be provided to enclose dry scaffolding which may be provided from the ground floor level of the building or if a canopy is provided at the first floor level, from the first floor level, up to the highest level (maximum four floors for this Project) of the scaffolding where scaffolding is erected around the perimeter of a building under construction;	N/A
• dump trucks for material transport should be totally enclosed using impervious sheeting;	✓
• any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading;	✓
• dusty materials remaining after a stockpile is removed should be wetted with water;	✓
• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with e.g. concrete, bituminous materials or hardcore or similar;	✓
• the portion of road leading only to a construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;	✓
• stockpile of dusty materials to be either covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides; or sprayed with water so as to maintain the entire surface wet;	✓
• all dusty materials to be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty material wet;	✓
• vehicle speed to be limited to 10 kph except on completed access roads;	✓
• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites;	✓
• the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;	✓
• the working area of excavation should be sprayed with water immediately before, during and immediately after (as necessary) the operations so as to maintain the entire surface wet;	✓
Odour mitigation measures	
• all malodorous excavated material should be placed as far as possible from any ASRs;	N/A
• the stockpiled malodorous material should be removed from site as soon as possible; and	N/A
• the stockpiled malodorous material should be covered entirely by plastic tarpaulin sheets.	N/A

Noise – Recommended Mitigation Measures

Noise Mitigation Measures during construction	Implementation Status
• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works;	✓

Noise Mitigation Measures during construction	Implementation Status
• machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;	✓
• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs;	✓
• silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction period;	N/A
• mobile plant should be sited as far away from NSRs as possible;	✓
• material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities;	N/A
• air compressor and hand-held breaker should be fitted with valid noise emission labels during operation; and	✓
• The Contractor shall at all times comply with all current statutory environmental legislation.	✓
Selection of quieter plant and working methods The Contractor shall obtain particular models of plant that are quieter than standards given in GW-TM. The list of assumed quieter plants can be found in the **Table 4–14** of the EIA report. The Contractor shall select from the available models achieving the assumed sound levels while making reference to the GW-TM and BS5228: Part 1: 1997	✓
Use of Noise Barriers Noise barriers are proposed along the site boundary to block the direct line of sight from the most affected NSRs to the major noise contribution construction phases. The height of the noise barriers ranged from 9-10m. The noise barriers shall be built before the commencement of construction works in order to ensure protection to nearby NSRs. The noise barrier should have a surface density of at least 10kg/m^2 or material providing equivalent transmission loss. The noise barriers and hoardings should have no gaps and openings to avoid noise leakage.	✓

Water Quality – Recommended Mitigation Measures

Water Quality Mitigation Measures during construction	Implementation Status
• The site should be confined to avoid silt runoff to the site.	✓
• No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site.	✓
• Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.	✓
• Stockpiles to be covered by tarpaulin to avoid spreading of materials during rainstorms;	✓
• Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;	✓
• Chemical waste containers shall be labelled with appropriate warning signs in English and Chinese to avoid accidents. there shall also be clear instructions showing what action to take in the event of an accidental;	✓
• Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area;	✓
• Any construction plant which causes pollution to the water system due to leakage of oil or fuel shall be removed off-site immediately;	N/A
• Spillage or leakage of chemical waste to be controlled by using suitable absorbent materials;	✓

Water Quality Mitigation Measures during construction	Implementation Status
• Chemicals will always be stored on drip trays or in bunded areas where the volume is 110% of the stored volume;	✓
• Regular clearance of domestic waste generated in the temporary sanitary facilities to avoid waste water spillage.	✓
• Temporary sanitary facilities to be provided for on-site workers during construction.	✓
• Temporary drainage channel and associated facilities will be provided to collect the surface runoff generated within the Project Area during the construction phase.	✓
• Sandbags or silt traps will need to be placed to avoid silt runoff to the drainage channel draining the water in the northern ditch. Draining of the ditches should avoid rainy weather.	✓
• Excavated soil which needs to be temporarily stockpiled should be stored in a specially designated area and provided with a tarpaulin cover to avoid runoff into the drainage channels.	✓

Waste Management – Recommended Mitigation Measures

Waste Management Mitigation Measures during construction	Implementation Status
Site Clearance Waste • The major construction works of Wo Shang Wai is in the development of residential buildings and other associated facilities (club house, tennis courts, etc). The amount of site clearance works will be limited with the exception of the excavated materials. The thin layer of vegetation removed can be stored and reused for landscaping.	✓
Excavated Materials The intention is to maximize the reuse of the excavated materials on-site as fill materials.	✓
Imported Filling Material The excavated/imported filling material may have to be temporarily stockpiled on-site for the construction of road embankment and foundation of viaduct substructure. Control measures should be taken at the stockpiling area to prevent the generation of dust and pollution of stormwater channels. However, to eliminate the risk of blocking drains in the wet season, it is recommended that stockpiling of excavated materials at during wet season should be avoided as far as practicable.	✓
Construction and Demolition Materials Careful design, planning and good site management can minimise over-ordering and generation of waste materials such as concrete, mortars and cement grouts. The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork of plastic facing should be considered to increase the potential for reuse.	✓
The Contractor should reuse any C&D material on-site. C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal.	✓
Chemical Waste For those processes which generate chemical waste, it may be possible to find alternatives which generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste.	N/A
Containers used for the storage of chemical wastes should:	
• be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed:	✓

Waste Management Mitigation Measures during construction	Implementation Status
• have a capacity of less than 450 litres unless the specification have been approved by the EPD; and	✓
• display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations,	✓
The storage area for chemical wastes should:	
• be clearly labelled and used solely for the storage of chemical waste;	✓
• be enclosed on at least 3 sides;	✓
• have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area whichever is the greatest;	✓
• have adequate ventilation;	✓
• be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and	✓
• be arranged so that incompatible materials are adequately separated.	✓
Disposal of chemical waste should:	
• be via a licensed waste collector; and	N/A
• be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers, or	N/A
• to be reuser of the waste, under approval from the EPD.	N/A
General Refuse Should be stored in enclosed bins or compaction units separate from C&D and chemical wastes. The Contractor should employ a reputable waste collector to remove general refuse from the site, separate from C&D and chemical wastes, on a regular basis to minimise odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.	✓
Disposal of Excavated Sediment at Sea	
The requirements and procedures for excavated sediment disposal are specified under the ETWB TCW No. 34/2002 and PNAP 252. The management of the excavation, use and disposal of sediment is monitored by Fill Management Committee, whilst the licensing of marine dumping is the responsibility of the Director of Environmental Protection (DEP).	N/A
The excavated sediment would be loaded onto barges or other appropriate vessel and transported to the designated marine disposal site. Category L sediment and Category M sediment passing the biological test would be suitable for disposal at a gazetted open sea disposal ground. Category M sediment failing the biological test and Category H sediment passing the biological test would require confined marine disposal.	N/A
During transportation and disposal of the dredged sediment, the following measures should be taken to minimize potential impacts on water quality: -	N/A
• Bottom opening transport vessels should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of vessels before the vessel is moved.	N/A
• Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP.	N/A

Ecology – Recommended Mitigation Measures

Ecology Mitigation Measures during construction	Implementation Status
Clear Definition of Site Limit	
Clear definition of the site limit should be provided in order to minimize and confine the disturbance during the construction period, especially the northern limit of the Site which is adjacent to fishponds within the Conservation Area (CA) zone and are considered to be ecological sensitive receivers. During wetland construction stage the WRA boundary will be delineated using a temporary hoarding in order to reduce disturbance to off-site habitats and wildlife. During the establishment phase this hoarding will be replaced with a 1 m high chain-link fence in order to reduce disturbance to the WRA through access by humans and dogs, and a hoarding will be established around the residential construction site.	✓ N/A
Dust and Noise Suppression and Avoidance of Water Pollution	
Good site practices of dust and noise suppression should be strictly implemented to ensure that disturbance is minimized to acceptable levels. Mitigation measures for the off-site disturbance impacts on the fishponds in the CA include hoarding at the northern site boundary during construction of the WRA to reduce noise and dust impacts to the adjacent habitats. Through the use of quieter plant and temporary/movable noise barriers, the noise level would be reduced significantly to an acceptable level. Hoarding at the northern boundary should be replaced with a 1 m high chain-link fence following construction and the WRA will then act as a buffer between the existing wetland areas and the residential part of the site until construction is completed. Hoarding will be retained between the WRA and ongoing construction work to avoid visual disturbance and reduce noise and dust emissions. Pollution of watercourses and sedimentary runoff will be minimized by good site practice, especially the containment of water and sediment within the site for removal. These standard noise and air and water quality site practices are considered to be effective measures for minimizing the disturbance impact during the construction period.	✓
Planning of Construction Schedule	
The construction of the proposed project should be scheduled in phases. Because mitigation is preferably carried out in advance of the main works rather than after the completion of works, the construction of the WRA will commence at the start of the project. Construction work within the WRA is scheduled to take place in a single wet season, followed by 1.5 years of wetland establishment. During the wetland establishment period no noisy work will be undertaken within the WRA to minimize the disturbance to off-site habitats and wildlife.	N/A
Reusing Onsite Materials	
Soil and plants on-site should be reused (e.g. used as fill material) as far as practical. Stock piles of these reusable materials should be stored in an appropriate area on-site. In particular, the re-use of the wetland soils and topsoil should be considered.	✓
Construction of the Wetland Restoration Area The WRA will be operational within 2.5 yrs from the commencement of construction (1 year for site formation and 1.5 years for establishment) and will compensate for the predicted ecological impacts of the proposed development.	✓

Landscape and Visual – Recommended Mitigation Measures

Landscape and Visual Mitigation Measures during construction	Implementation Status
CM1 - The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape.	✓
CM2 - Screening of construction works by hoarding / noise barriers.	✓
CM3 - Reduction of construction period to practical minimum.	✓
CM4 - Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where the soil material meets acceptable criteria and where practical. The Contract Specification shall include storage and reuse of topsoil as appropriate.	✓
CM5 - Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone).	✓
CM6 – Advance screen planting of noise barriers	✓
CM7 - Control night-time lighting and glare by hooding all lights.	N/A
CM8 - Ensure no run-off into streams adjacent to the Project Area.	✓
CM9 - Protection of existing trees on boundary of site shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at S16 and Tree Removal Application stage).	✓
CM10 - Trees unavoidably affected by the works shall be transplanted where practical. Trees should be transplanted straight to their destinations and not held in a nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.	✓

Legend:

✓	Implemented
×	Not implemented
P	Partially implemented
N/A	Not applicable
