MOTT MACDONALD

Proposed Comprehensive Development at Wo Shang Wai, Yuen Long

Monthly EM&A Report for March 2022

8 April 2022

Mott MacDonald
3/F Manulife Place
348 Kwun Tong Road
Kwun Tong
Kowloon
Hong Kong

T +852 2828 5757
F +852 2827 1823
mottmac.hk

Profit Point Enterprises Limited

Proposed Comprehensive Development at Wo Shang Wai, Yuen Long

Monthly EM&A Report for March 2022

8 April 2022

Mott MacDonald Hong Kong Limited
registered in Hong Kong no. 236497

Document reference: 370161 | 05|01 | A

Information class: Standard

This document is issued for the party which commissioned it and for specific purposes connected with the above-captioned project only. It should not be relied upon by any other party or used for any other purpose.

We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

This document contains confidential information and proprietary intellectual property. It should not be shown to other parties without consent from us and from the party which commissioned it.

Pursuant to Condition 4.5 of Environmental Permit No. EP-311/2008/E, this Monthly EM&A Report for March 2022 has been reviewed, certified by Environmental Team Leader (ETL) and verified by the Independent Environmental Checker (IEC).

Certified by:

Eugenne Yuen
Environmental Team Leader (ETL)
Mott MacDonald Hong Kong Ltd.

Date 14 April 2022

Verified by:

David Yeung
Independent Environmental Checker (IEC)
Ramboll Hong Kong Limited

Date 14 April 2022

Contents

Executive summary 1

1 Introduction 2
1.1 Introduction 2
1.2 Project Organization 2
1.3 Environmental Status in the reporting period 2
1.4 Summary of EM&A Requirements 3

2 Impact Monitoring Methodology 5
2.1 Introduction 5
2.2 Air Quality 5
2.3 Construction Noise 7
2.4 Water Quality 9
2.5 Ecology 11
2.6 Landscape and Visual 12

3 Monitoring Results 15
3.1 Impact Monitoring Schedule 15
3.2 Results of Impact Monitoring 15

4 Ecological Monitoring 24
4.1 Monitoring of Birds 24
4.2 Monitoring of Herpetofauna 24
4.3 Monitoring of Dragonflies and Butterflies 24
4.4 Monitoring of Mammals 25
4.5 Monitoring of Water Quality 25
4.6 Management Activities 25
4.7 Summary 26

5 Landscape and Visual 28
5.1 Site Inspections 28
5.2 Construction Phase Audit Summary 28

6 Environmental Site Inspection and Audit 30
6.1 Site Inspection 30
6.2 Solid and Liquid Waste Management Status 30
6.3 Status of Environmental Licences and Permits 30
6.4 Recommended Mitigation Measures 30

7 Report on Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions 32
7.1 Record of non-compliance of Action and Limit Levels 32
7.2 Record on Environmental Complaints Received 32
7.3 Record on Notifications of Summons and Successful Prosecution 32
7.4 Review of Reasons for and Implications of Non-compliance, Complaints, Summons and Prosecutions 32
7.5 Follow-up Actions Taken 33
7.6 Cumulative Statistics for Complaints, Notifications of Summons and Successful Prosecutions 33

8 Future Key Issues 34
8.1 Site Preparatory Works and Construction Works for the Coming Month 34
8.2 Key Issues for the Coming Months 34
8.3 Monitoring Schedule for the Coming Month 34
8.4 Conclusions and Recommendations 35

Appendices 39

A. Project Organization Chart 41

B. Tentative Construction Programme (not used) 43

C. Action and Limit Levels for Construction Phase 45

D. Event and Action Plan for Air Quality, Noise, Water Quality and Landscape & Visual 47

E. Calibration Certificates 53

F. Graphical Plots of the Monitoring Results 55

G. Weather Conditions during the Monitoring Period 57

H. Ecological Monitoring conducted 59

I. Summary of Bird Surveys conducted 61

J. Summary of Herpetofauna, Mammal and Insect Surveys conducted 67

K. Summary of Water Quality Monitoring associated with Ecological Monitoring conducted 71

L. Environmental Mitigation Measures - Implementation Status 73

M. Landscape and Visual Audit Photos 79

Tables

Table 1.1: Summary of Impact EM&A Requirements 3
Table 1.2: Environmental Monitoring and Audit Schedule for the Reporting Month 4
Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration 5
Table 2.2: Air Monitoring Stations 5
Table 2.3: TSP Monitoring Equipment 6
Table 2.4: Noise Monitoring Parameters, Frequency and Duration 8
Table 2.5: Noise Monitoring Stations 8
Table 2.6: Noise Monitoring Equipment 8
Table 2.7: Water Quality Monitoring Parameters, Frequency and Duration 9
Table 2.8: Water Quality Monitoring Stations 9
Table 2.9: Water Quality Monitoring Equipment 10
Table 2.10: Analytical Methods applied to Water Quality Samples 10
Table 2.11: Detection Limits for Water Quality Determinants 10
Table 2.12: Summary of Construction Phase Ecological Monitoring for the Wo Shang Wai Wetland Restoration Area (WRA) 12
Table 2.13: Construction and Operation Phase Audit Checklist 13
Table 2.14: Proposed Construction Phase Mitigation Measures 13
Table 2.15: Proposed Operation Phase Mitigation Measures 14
Table 3.1: Summary of 1-hour TSP Monitoring Results 15
Table 3.2: Summary of 24-hour TSP Monitoring Results 16
Table 3.3: Summary of Construction Noise Monitoring Results 17
Table 3.4: Summary of Water Quality Monitoring Results 18
Table 4.1: Summary of Ecological Monitoring in WRA and Survey Area under EM&A Manual 26
Table 5.1: Construction and Operation Phase Audit Summary 28
Table 6.1: Summary of Site Inspections and Recommendations 30
Table 6.2: Status of Environmental Submissions, Licences and Permits 30
Table 7.1: Summary of Exceedances in Water Quality 32
Table 7.2: Statistics for Complaints, Notifications of Summons and Successful Prosecution 33
Table 8.1: Tentative Environmental Monitoring and Audit Schedule for the Next Reporting Month 35

Figures

Figure 1.1 General Layout Plan of the Project Site
Figure 2.1 Locations of Air Quality Monitoring Stations

Figure 2.2 Locations of Noise Monitoring Stations
Figure 2.3 Locations of Water Quality Monitoring Stations
Figure 4.1 Survey Area and Transect Walked
Figure 4.2 Water Quality Monitoring Locations for Ecological Monitoring

Executive summary

Mott MacDonald Hong Kong Ltd. ("MMHK") has been commissioned by the Contractor, Heng Shung Construction Co. Ltd., to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit (EM&A) for both pre-construction and construction phases of the Proposed Comprehensive Development at Wo Shang Wai, Yuen Long. From August 2016, the Project Proponent, Profit Point Enterprises Limited, commissioned MMHK to continue the ET services.

This is the 143rd EM&A report submitted under the Condition 4.5 of Environmental Permit No. EP-311/2008/E. This report summarises the findings on EM&A during the period from 1 to 31 March 2022.

Exceedance of Action and Limit Levels

There was no breach of Action or Limit levels for Air Quality (1-hr TSP and 24-hr TSP) and Noise level (as L_{eq}) in the reporting month.

During March 2022, three Limit Level exceedances of suspended solids (SS) were observed. One Limit Level exceedance of SS was recorded at MP3 and two Limit Level exceedances of SS were recorded at MP4.

Implementation of Mitigation Measures

Site audits were carried out on 2, 11, 16 and 25 March 2022 to confirm the implementation measures undertaken by the Contractor in the reporting month. The outcomes are presented in Section 6 and the status of implementation of mitigation measures in the site is shown in **Appendix L**.

Record of Complaints

There was no record of complaints received in the reporting month.

Future Key Issues

Site works scheduled to be commissioned in the coming three months include regular maintenance work for the Wetland Restoration Area including lowering of the water level and removal of unwanted species in the pond. No major construction works will be carried out. Potential environmental impacts due to the activities, including air quality, noise, water quality, ecology and landscape and visual, will be monitored.

Environmental mitigation measures will be implemented on site as recommended and weekly site audits will be carried out to ensure that the environmental conditions are acceptable.

1 Introduction

1.1 Introduction

In March 2005, the Project Proponent, Profit Point Enterprises Limited, acquired the development site at Wo Shang Wai in Yuen Long. An Environmental Impact Assessment (EIA) was then carried out and approved under the EIA Ordinance (EIAO), and the Environmental Permit (EP-311/2008) for construction of the comprehensive development in Wo Shang Wai was first granted by EPD on 9 September 2008 and has been subsequently varied, with the current version (EP-311/2008/E) issued by EPD on 19 December 2017.

The Project involves the residential development and associated infrastructure and wetland restoration area and linear landscape area. The construction works under the Environmental Permit commenced on 12 May 2010. The site formation construction works of the Wetland Restoration Area (hereafter WRA) were completed on 15 November 2010 and the WRA was established by October 2012, within 30 months from the commencement of construction as stipulated in the EP. This indicated that planting works as scheduled in the approved Wetland Restoration and Creation Scheme (WRCS; Nov 2009) were complete, except along the western and southern boundary where the planting is affected by the existing site boundary and noise barrier, and for which a Variation to Environmental Permit (EP-311/2008/C) to defer planting at the location was approved. Consequently, EP (EP-311/2008/D) including specific mitigation measures to minimise certain identified noise impacts during the operation phase was approved. The current valid EP (EP-311/2008/E) comprises varied conditions for the implementation and maintenance of visual and landscape measures, and for the implementation of noise mitigation measures.

Mott MacDonald Hong Kong Ltd. (“MMHK”) has been commissioned by the Contractor, Heng Shung Construction Co. Ltd., to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit (EM&A) for both pre-construction and construction phases of the Proposed Comprehensive Development at Wo Shang Wai, Yuen Long. From August 2016, the Project Proponent, Profit Point Enterprises Limited, commissioned MMHK to continue the ET services.

According to the EP Condition 4.5, the monthly EM&A Report shall be submitted to the Director within two weeks after the end of the reporting month. This report summarises the findings during the period from 1 to 31 March 2022.

1.2 Project Organization

The organisation chart and lines of communication with respect to the on-site environmental management structure together with the contact information of the key personnel are shown in **Appendix A**.

1.3 Environmental Status in the reporting period

During the reporting month, construction works of the Project undertaken include:

- General site maintenance work

- Regular maintenance work for the Wetland Restoration Area (including lowering of the water level and removal of unwanted species in the pond)

There were no major construction works carried out. The general layout plan of the Project site is shown in **Figure 1.1**.

1.4 Summary of EM&A Requirements

The EM&A programme requires environmental monitoring of air quality, noise, water quality, ecology and landscape and visual as specified in the approved EM&A Manual.

A summary of impact EM&A requirements is presented in **Table 1.1** below:

Table 1.1: Summary of Impact EM&A Requirements

Parameters	Descriptions	Locations	Frequencies
Air Quality	24-Hour TSP	ASR1, ASR2A, ASR3, ASR4	Once every 6 days
	1-Hour TSP	ASR1, ASR2A, ASR3, ASR4	3 times every 6 days
Noise	$L_{eq(30min)}$, L_{90}, L_{10} (dB(A))	NSR1, NSR3, NSR5, NSR7	Weekly
Water Quality	Dissolved Oxygen (DO), temperature, pH, suspended solids (SS) and Biochemical Oxygen Demand (BOD)	MP1 to MP6	3 days per week
Ecology	Birds	Within the Project Area and Assessment Area of 500m	Weekly
	Dragonflies and Butterflies	Within the Project Area and Assessment Area of 500m	Once per month during Mar and Sep to Nov, and twice per month during Apr to Aug
	Herpetofauna	Within the Project Area and Assessment Area of 500m	Daytime: Once per month during Apr to Nov Night-time: Once per month during Mar to Aug
	Water quality of Wetland Restoration Area (WRA)	WRA	After filling of WRA with water, monthly for in situ water quality and every six months (end of wet season and end of dry season) for laboratory testing
	Site Inspections	Within the Project Area and Assessment Area of 500m	Weekly
Landscape and Visual	Auditing of protection of existing trees, the transplanting of existing trees, the creation of new wetland, the planting of new trees and shrubs and other landscape and visual mitigation measures	CM1 to CM10 and OM1 to OM7 within the Project Area	Site inspections once every two weeks during construction phase; once every two months during operational phase

The Environmental Quality Performance Limits for air quality, noise and water quality are shown in **Appendix C**.

The Event and Action Plan for air quality, noise, water quality and Landscape & Visual are shown in **Appendix D**.

The monitoring schedule for the reporting month is shown in **Table 1.2** as follows.

Table 1.2: Environmental Monitoring and Audit Schedule for the Reporting Month

Tentative Environmental Monitoring and Audit Schedule for March 2022

Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2 Water *	3 **Bird**	4 Water 24-hr TSP 1-hr TSP	5
6	7 Water	8	9 Water	10 **Bird** 24-hr TSP 1-hr TSP Noise Monitoring	11 Water * **Landscape**	12
13	14 Water @	15 **Water Quality Monitoring** **Herpetofauna (daytime)**	16 Water * 24-hr TSP 1-hr TSP Noise Monitoring	17 **Bird** **Dragonfly & Butterfly**	18 Water	19
20	21 Water **Bird**	22 **Water Quality Monitoring** 24-hr TSP 1-hr TSP Noise Monitoring	23 Water	24	25 Water * **Landscape**	26
27	28 Water 24-hr TSP 1-hr TSP Noise Monitoring	29 **Bird** **Water Quality Monitoring** **Herpetofauna (night-time)**	30 Water	31		

* Site Audit by Mott MacDonald (MM)

@ Report Submission (Monthly EM&A Report)

Ecological Surveys & Landscape Audits indicated in **bold font**

2 Impact Monitoring Methodology

2.1 Introduction

For air quality, construction noise and water quality, ecology, landscape and visual monitoring methodology, including the monitoring locations, monitoring equipment used, monitoring parameters, and frequency and duration, etc., are detailed in this Chapter.

2.2 Air Quality

2.2.1 Monitoring Parameters, Frequency and Duration

In accordance with the EM&A Manual, 1-hour and 24-hour TSP levels monitoring are to be conducted during the construction phase. **Table 2.1** summarizes the monitoring parameters, frequency and duration of air quality monitoring.

Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
ASR1, ASR2A, ASR3 & ASR4	24-hour TSP	At least once in every six-days
	1-hour TSP	3 times every six-days

2.2.2 Monitoring Locations

The four air quality monitoring stations were established in the EM&A manual and were slightly adjusted during the baseline monitoring phase. Locations of the agreed air quality monitoring stations are listed in **Table 2.2** and as shown in **Figure 2.1**.

Table 2.2: Air Monitoring Stations

Monitoring Stations	Locations
ASR1	Guard house outside House No. 1, Ventura Avenue, Royal Palms*
ASR2A	At the rooftop of refuse collection point, which is located at the southwest of the project area
ASR3	At the commercial centre at Palm Springs, which is located at the south of the project area
ASR4	Outside works site entrance*

*Note: Relocation of ASR1 and ASR4 were from 5 June 2018 as the previous locations will be subject to upcoming construction works. All monitoring data at ASR1 and ASR4 from June 2018 is measured at the new monitoring locations.

2.2.3 Monitoring Equipment

Continuous 24-hour TSP air quality monitoring is conducted using High Volume Sampler (HVS) (Model: GMWS-2310 Accu-vol). The HVS meets all the requirements of the EM&A Manual. Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. **Table 2.3** summarizes the equipment used in the impact air quality monitoring.

Table 2.3: TSP Monitoring Equipment

Equipment	Model
24-hr TSP monitoring	
High Volume Sampler	GMWS 2310 Accu-vol
Calibrator	TE-5025A
1-hr TSP monitoring	
Portable direct reading dust meter	Sibata LD-3B Laser Dust Monitor

2.2.4 Monitoring Methodology

2.2.4.1 24-hour TSP Monitoring

Installation

The HVS was installed in the vicinity of the air sensitive receiver. The following criteria were considered in the installation of the HVS.

- A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
- The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
- A minimum of two metres separation from walls, parapets and penthouse was required for rooftop sampler.
- A minimum of two metres separation from any supporting structure, measured horizontally was required.
- No furnace or incinerator flues or building vent were nearby.
- Airflow around the sampler was unrestricted.
- The sampler has been more than 20 metres from any drip line.
- Permission was obtained to set up the samplers and to obtain access to the monitoring stations.
- A secured supply of electricity is needed to operate the samplers.

Preparation of Filter Papers

- Glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected.
- All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C with relative humidity (RH) < 50% and was not variable by more than ±5%. A convenient working RH was 40%.

Field Monitoring

- The power supply was checked to ensure the HVS works properly.
- The filter holder and the area surrounding the filter were cleaned.
- The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
- The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
- The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges.

- The shelter lid was closed and was secured with the aluminium strip.
- The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
- A new flow rate record sheet was set into the flow recorder.
- The flow rate of the HVS was checked and adjusted at around 1.1 m^3/min. The range specified in the EM&A Manual was between 0.6-1.7 m^3/min.
- The programmable timer was set for a sampling period of 24 hrs + 1 hr, and the starting time, weather condition and the filter number were recorded.
- The initial elapsed time was recorded.
- At the end of sampling, the sampled filter was removed carefully and folded in half-length so that only surfaces with collected particulate matter were in contact.
- It was then placed in a clean plastic envelope and sealed.
- All monitoring information was recorded on a standard data sheet.
- Filters were sent to a HOKLAS accredited laboratory for analysis.

Maintenance and Calibration

- The HVS and its accessories are maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVSs were calibrated at two-month intervals.
- Calibration records for HVSs are shown in **Appendix E**.

2.2.4.2 1-hour TSP Monitoring

Field Monitoring

The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

- Set POWER to "ON", push BATTERY button, make sure that the meter's indicator is in the range with a red line and allow the instrument to stand for about 3 minutes (Then, the air sampling inlet has been capped).
- Push the knob at MEASURE position.
- Push "O-ADJ" button. (Then meter's indication is 0).
- Push the knob at SENSI ADJ position and set the meter's indication to S value described on the Test Report using the trimmer for SENSI ADJ.
- Pull out the knob and return it to MEASURE position.
- Push "START" button.

Maintenance and Calibration

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are shown in **Appendix E**.

2.3 Construction Noise

2.3.1 Monitoring Parameters, Frequency and Duration

Following the requirements in the EM&A Manual for noise, noise monitoring has to be carried out during the construction phase. Continuous noise monitoring for the A-weighted levels $L_{eq(30\ min)}$, L_{10} and L_{90} is undertaken once per every week.

Table 2.4 summarizes the monitoring parameters, frequency and duration of air quality monitoring.

Table 2.4: Noise Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
NSR1, NSR3, NSR5, NSR7	$L_{eq(30min)}$, L_{90}, L_{10} (dB(A))	Once every week

2.3.2 Monitoring Locations

The four noise quality monitoring stations were established in the EM&A manual and were slightly adjusted during the baseline monitoring phase. Locations of the agreed noise quality monitoring stations are listed in **Table 2.5** and as shown in **Figure 2.2**.

Table 2.5: Noise Monitoring Stations

Monitoring Stations	Locations	Type of measurement
NSR1	Noise monitoring equipment was set up near the boundary wall at Palm Springs	Free field
NSR3	The monitoring station was located next to the guard house at Palm Spring	Façade
NSR5	Outside House No. 1, Ventura Avenue, Royal Palms*	Façade
NSR7	The monitoring station was located near the boundary wall of the house of Mai Po San Tsuen	Free field

*Note: Relocation of NSR5 was from 5 June 2018 as the previous location will be subject to upcoming construction works. All monitoring data at NSR5 from June 2018 is measured at the new monitoring location.

2.3.3 Monitoring Equipment

Integrating Sound Level Meter will be used for noise monitoring. It is a Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They comply with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 2.6** summarizes the noise monitoring equipment model being used.

Table 2.6: Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-52
Calibrator	Larson Davis CAL200

2.3.4 Monitoring Methodology

Field Monitoring

- The Sound Level Meter was set on a tripod at a height of at least 1.2 m above the ground.
- Façade and free-field measurements were made at the monitoring locations.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting: A
  - time weighting: Fast

  - time measurement: 30 minutes intervals (between 07:00 and 19:00)
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid has to be repeated after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq}, L_{10} and L_{90} were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.

Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix E**.

2.4 Water Quality

2.4.1 Monitoring Parameters, Frequency and Duration

In accordance with the requirements in the EM&A Manual for water quality, water quality parameters including Dissolved Oxygen (DO), temperature, pH, turbidity, suspended solids (SS) and Biochemical Oxygen Demand (BOD) have to be monitored at designated monitoring stations during construction of the Project. DO, temperature and pH were measured in-situ whereas SS and BOD were analysed in a laboratory. The measurements should be taken at all designated monitoring stations, three days per week. The interval between any two sets of monitoring was not less than 36 hours. **Table 2.7** summarizes the monitoring parameters, frequency and duration of water quality monitoring.

Table 2.7: Water Quality Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Frequency and Duration
MP1, MP2, MP3, MP4, MP5 & MP6	DO, temperature, pH, SS, turbidity, BOD	Three days every week

2.4.2 Monitoring Locations

The six water quality monitoring stations were established in the EM&A manual. Locations of the agreed water quality monitoring stations are listed in **Table 2.8** and as shown in **Figure 2.3**.

Table 2.8: Water Quality Monitoring Stations

Monitoring Stations	Easting	Northing
MP1*	838 730.50	822 862.25
MP2*	838 933.26	823 247.41
MP3	839 107.17	823 596.84
MP4	839 286.14	823 638.55
MP5	839 134.35	823 722.99
MP6	839 063.02	823 842.25

*Note: The water quality impact monitoring at MP1 and MP2 have been terminated since July 2012 due to withdrawal of access right from landowner.

2.4.3 Monitoring Equipment

The Water Quality Monitoring Equipment and Analytical Methods applied to Water Quality Samples are given in **Table 2.9** and **Table 2.10** respectively. Details of which are discussed as follows.

Table 2.9: Water Quality Monitoring Equipment

Equipment	Model	Equipment/ Serial Number
Conductivity, Dissolved oxygen, pH, Salinity and Temperature Measuring Meter, Turbidity	YSI ProDSS	17E100747 16H104233 16H104234
Global Positioning System (GPS)	Garmin eTrex Vista	ENO 007

Table 2.10: Analytical Methods applied to Water Quality Samples

Determinant, unit	Standard Method
Total Suspended Solids, mg/L	In house method based on APHA 2540D; ALS Method Code: EA-025
Biochemical Oxygen Demand (BOD), mg/L	In house method based on APHA 5210B; ALS Method Code: EP-030

All in-situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme before use.

Dissolved Oxygen (DO), Temperature, pH and Turbidity measuring equipment

A portable, weatherproof multiparameter instrument (YSL ProDSS) was used in the monitoring. It can be capable for measuring dissolved oxygen (DO), temperature, pH and turbidity simultaneously with the following limits:

- a dissolved oxygen level in the range of 0-50 mg/L and 0-500 % saturation;
- a temperature of -5 to 70 degrees Celsius;
- pH value of 0-14 with 0.1 as the base unit; and
- turbidity between 0-4000 NTU

Global Positioning System (GPS)

A hand-held GPS navigator (Garmin eTrex Vista) was used to identify the designated monitoring stations prior to water sampling.

Suspended Solids and BOD Measurements (Sample Containers and Storage)

Water samples for SS analysis were stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4 ºC without being frozen), delivered to the laboratory, and analysed as soon as possible after collection. Analysis was carried out in a HOKLAS accredited laboratory.

2.4.4 Detection Limit

The limits of detection for the in-situ and laboratory measurements are shown in **Table 2.11**.

Table 2.11: Detection Limits for Water Quality Determinants

Determinant	Limit of Detection
Dissolved Oxygen	0.1 mg/L
Temperature	0.1 degree Celsius

Determinant	Limit of Detection
pH	0.01 unit
Turbidity	0.1 NTU
Suspended Solids	2 mg/L
BOD	2 mg/L

2.4.5 Monitoring Methodology

In situ Measurement

All pH meters, DO/ temperature meters had been checked and calibrated prior to use. Standard buffer solution of at least two pH levels (either pH 4 and pH 7, or pH 7 and pH 10) had been used for calibration of the instrument before and after use.

DO meters had been calibrated by a laboratory accredited under HOKLAS or any other international accreditation scheme, and subsequently re-calibrated at three-monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes had been checked with certified standard solutions before each use. Wet bulb calibrations for all DO meters had been carried out before measurement at each monitoring location. For the on-site calibration of field equipment, BS 1427:2009, "Guide to on-site test methods for the analysis of waters" had been observed.

Measurements shall be at three water depths, namely, 1m below water surface, mid-depth and 1m above stream bed/pond bed, except where the water depth less that 6m, the mid-depth station maybe omitted. Should the water depth be less than 3 m, only the mid-depth station will be monitored.

Replicates in-situ measurements and samples collected from each independent monitoring event are required for all parameters to ensure a robust statistically interpretable dataset.

Water Samples Preparation and Analysis

For collection of water sampling within the water courses, a 500ml clean plastic beaker was used. After collection, the water samples were stored in high-density polythene bottles. The sample container was rinsed with a portion of the water sample. The water sample was then transferred to the container, labelled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4 ºC. The water samples were then delivered to a local HOKLAS-accredited laboratory (ALS) on the same day for analysis.

The testing methods of testing parameters as recommended by EIA or required by EPD, with the QA/QC results are in accordance with the requirement of HOKLAS or international accredited scheme.

The calibration certificates for equipment used for in-situ monitoring of water quality are attached in **Appendix E**.

2.5 Ecology

2.5.1 Monitoring Parameters, Frequency and Duration

Target species and certain other fauna will be monitored within the Project Area and Assessment Area during the wetland and residential construction phase. This will be important to ensure that any unexpected events or impacts either on- or off-site are quickly identified so that remedial action can be taken. The groups to be monitored and frequency of monitoring are shown in **Table 2.12**.

Table 2.12: Summary of Construction Phase Ecological Monitoring for the Wo Shang Wai Wetland Restoration Area (WRA)

Species / Parameter	Construction Phase Ecological Monitoring
Birds	Weekly (including Assessment Area)
Dragonflies and Butterflies	Once per month during March and September to November; and twice per month during April to August
Herpetofauna	Daytime: Once per month during April to November; and Night-time: Once per month during March to August
Water Quality	After filling of WRA with water, monthly for in situ water quality and every six months (end of the wet season and end of the dry season) for laboratory testing
Site Inspections	Weekly

2.5.2 Monitoring Locations and Methodology

Ecological monitoring locations during construction phase are shown in **Figure 4.1** and the methodology for ecological monitoring is detailed in **Section 4**.

2.6 Landscape and Visual

2.6.1 Monitoring Parameters, Frequency and Duration

All measures undertaken by both the Contractor and the specialist Landscape Sub-Contractor during the construction phase and first year of the operational phase shall be audited by a Registered Landscape Architect, as a member of the ET, on a regular basis to ensure compliance with the intended aims of the measures. Site inspections should be undertaken at least once every two weeks throughout the construction period and once every two months during the operational phase.

The broad scope of audit is detailed below but should also be undertaken with reference to the more specific checklist provided in **Table 2.13** below. Operational phase auditing will be restricted to the last 12 months of the establishment works of the landscaping proposals and thus only the items below concerning this period are relevant to the operational phase.

- The extent of the agreed works area should be regularly checked during the construction phase. Any trespass by the Contractor outside the limit of the works, including any damage to existing trees and woodland shall be noted;
- The progress of the engineering works should be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken;
- All existing vegetation, streams and other features within the study area which are not directly affected by the works are retained and protected;
- The methods of protecting existing vegetation proposed by the Contractor are acceptable and enforced;
- Preparation, lifting transport and re-planting operations for any transplanted trees;
- The layout, design and construction of buildings conforms to requirements specified in the EIA report;
- All landscaping works are carried out in accordance with the EIA recommendations and with specifications;
- The planting of new trees, shrubs, groundcover, climbers, grasses and other plans, together with the replanting of any transplanted trees are carried out properly and within the right season;

- All necessary horticultural operations and replacement planting are undertaken throughout the Establishment Period to ensure the healthy establishment and growth of both transplanted trees and all newly establishment plants.

Table 2.13: Construction and Operation Phase Audit Checklist

Area of Works	Items to be Monitored
Works Area	Check the extent of the Works to ensure that the Works Area is not exceeded the site boundaries.
Protection of all trees and woodland blocks to be retained	Identification and demarcation of trees / vegetation to be retained, erection of physical protection (e.g. fencing), monitoring against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Streams	Ensure no run-off into existing streams
Clearance of existing vegetation	Identification and demarcation of trees / vegetation to be cleared, checking of extent of works to minimize damage, monitoring of adjacent areas against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Transplanting of trees	Identification and demarcation of trees / vegetation to be transplanted, monitoring of extent of pruning / lifting works to minimize damage, timing of operations implementation of all stages of preparatory and translocation works, and maintenance of transplanted vegetation, etc.
Topsoil stripping	Ensuring existing topsoil is stripped and stored under recognized good practice and is hydroseeded and regularly turned to prevent anaerobic conditions
New buildings	Ensure that building finishes accord with mitigation proposals with regard to colour and albedo.
Boundaries	Ensuring hoarding are erected as required
Noise Barrier	Ensure noise barrier design accords with the mitigation proposals with regard to location, materials and finishes.
Night-time lighting	Ensuring night-time lighting is directional, hooded and shielded away from VSRs
Plant supply	Monitoring of operations relating to the supply of specialist plant material (including the collecting, germination and growth of plants from seed) to ensure that plants will be available in time to be used within the construction works.
Landscape and wetland treatments generally	Check that wetland, and hard / soft landscape designs conform to intent of mitigation measures and agreed designs
Soiling, planting, etc.	Monitoring of implementation and maintenance of soiling and planting works against possible incursion, physical damage, fire, pollution, surface erosion, etc.
Establishment Works	Monitoring of implementation of maintenance operation during Establishment Period

2.6.2 Monitoring Locations

The monitoring locations should check against the mitigation measures proposed under the approved Environmental Impact Assessment, which are summarised as follows in **Table 2.14** and **Table 2.15**:

Table 2.14: Proposed Construction Phase Mitigation Measures

ID No.	Landscape and Visual Mitigation Measures
CM1	The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape.
CM2	Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colours, to screen Works.
CM3	Reduction of construction period to practical minimum.
CM4	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where the soil material meets acceptable criteria and where practical. The Contract Specification shall include storage and reuse of topsoil as appropriate.
CM5	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone).
CM6	Advance screen planting to noise barriers.

ID No.	Landscape and Visual Mitigation Measures
CM7	Control night-time lighting and glare by hooding all lights.
CM8	Ensure no run-off into streams adjacent to Project Area.
CM9	Protection of existing trees on boundary of project area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at S16 and Tree Removal Application stage).
CM10	Trees unavoidably affected by the works shall be transplanted where practical. Trees should be transplanted straight to their destinations and not held in a nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.

Table 2.15: Proposed Operation Phase Mitigation Measures

ID No.	Landscape Mitigation Measures
OM1	Compensatory Tree Planting for all felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under DEVB TC(W) 7/2015.
OM2	A continuous belt of screen planting along southern perimeter of project area with fast growing tree species. At least 450 trees capable of reaching a height > 10m within 10 years should be planted. Planting of the belt of trees shall be carried out as advance works ahead of other site formation and building works.
OM3	Maximise soft landscape and amenity water bodies in residential areas of the development. Approximately 750 trees (of Heavy Standard size) should be planted. Where space permits, roadside berms should be created. Street trees should be of species that reach a mature height of no less than 15m.
OM4	Maximise freshwater habitat wetland creation consistent with achieving other parameters. Minimum 4.74 ha to be provided. Wetlands must have natural edge profiles with >1m wide emergent zone. No access to the wetland by residents and all wetlands must be screened from residential development by a continuous tree screen at interface with residential development or earth mounding such that disturbance is minimised. Implementation of the wetland shall be carried out as advance works.
OM5	Use appropriate (visually unobtrusive and non-reflective) building materials and colours in built structures.
OM6	During detailed design, refine building layout to create a min. 10m wide gap between buildings north of Wo Shang Wai pond and also two min. 10m wide gaps in the row of buildings adjacent to Royal Palms.
OM7	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimise unnecessary light spill.

3 Monitoring Results

3.1 Impact Monitoring Schedule

Impact monitoring for air quality (dust), noise and water quality due to the construction work were undertaken during the reporting month in compliance with the EM&A manual in the reporting period. Regular site inspections were carried out on 2, 11, 16 and 25 March 2022 during the reporting month to assess the compliance with environmental requirements.

3.2 Results of Impact Monitoring

3.2.1 Air Quality Monitoring

3.2.1.1 1-hour TSP

Results of 1-hour TSP at the four monitoring locations are summarised in **Table 3.1**. Graphical plots of the monitoring results are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.1: Summary of 1-hour TSP Monitoring Results

Monitoring Date	Start Time	1-hr TSP (μg/m³)			Range (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
		1st Result	2nd Result	3rd Result			
ASR1							
04-Mar-22	09:22	64	46	30	12-64	378	500
10-Mar-22	08:56	14	13	12			
16-Mar-22	08:40	22	21	21			
22-Mar-22	08:33	47	64	57			
28-Mar-22	08:33	26	33	34			
ASR2A							
04-Mar-22	13:20	60	50	32	19-71	357	500
10-Mar-22	13:07	22	20	19			
16-Mar-22	13:00	21	22	22			
22-Mar-22	13:08	58	71	65			
28-Mar-22	13:00	27	30	34			
ASR3							
04-Mar-22	13:02	56	48	32	12-74	358	500
10-Mar-22	13:22	15	12	12			
16-Mar-22	13:18	20	27	20			
22-Mar-22	13:27	61	74	70			
28-Mar-22	13:18	35	38	37			

Monitoring Date	Start Time	1-hr TSP (μg/m³)			Range (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
		1st Result	2nd Result	3rd Result			
ASR4							
04-Mar-22	09:04	69	47	32	13-77	372	500
10-Mar-22	09:12	16	15	13			
16-Mar-22	08:59	29	29	28			
22-Mar-22	08:54	56	77	73			
28-Mar-22	08:53	29	28	30			

3.2.1.2 24-hour TSP

Results of 24-hour TSP at the four monitoring locations are summarised in **Table 3.2**. Graphical plots of the monitoring results are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.2: Summary of 24-hour TSP Monitoring Results

Monitoring Date	Monitoring Results (μg/m³)	Range (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
ASR1				
04-Mar-22	32	23-49	226	260
10-Mar-22	49			
16-Mar-22	36			
22-Mar-22	30			
28-Mar-22	23			
ASR2A				
04-Mar-22	63	37-63	213	260
10-Mar-22	40			
16-Mar-22	37			
22-Mar-22	41			
28-Mar-22	40			
ASR3				
04-Mar-22	61	25-61	205	260
10-Mar-22	50			
16-Mar-22	36			
22-Mar-22	25			
28-Mar-22	31			
ASR4				
04-Mar-22	72	13-72	237	260
10-Mar-22	50			
16-Mar-22	45			
22-Mar-22	35			
28-Mar-22	13			

No exceedance of 1-hour and 24-hour TSP (Action or Limit Level) was recorded in the reporting period.

3.2.2 Construction Noise Monitoring

The construction noise monitoring results are summarized in **Table 3.3**. Graphical plots of the monitoring data are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.3: Summary of Construction Noise Monitoring Results

Monitoring Date	Start Time	Mean and Range of Noise Levels, dB(A)			Limit Level for L_{eq} (dB(A))
		L_{eq}	L_{10}	L_{90}	
NSR1					
10-Mar-22	11:28	49	50	44	75
16-Mar-22	11:25	49	51	42	
22-Mar-22	11:18	48	51	41	
28-Mar-22	11:16	48	50	40	
NSR3					
10-Mar-22	10:44	46	49	42	75
16-Mar-22	10:41	49	51	42	
22-Mar-22	10:35	44	48	40	
28-Mar-22	10:31	46	49	41	
NSR5					
10-Mar-22	10:01	50	53	46	75
16-Mar-22	09:54	48	49	45	
22-Mar-22	09:47	47	49	44	
28-Mar-22	09:44	50	52	46	
NSR7					
10-Mar-22	09:16	66	68	64	75
16-Mar-22	09:03	66	68	63	
22-Mar-22	08:58	67	69	64	
28-Mar-22	08:57	67	69	64	

No exceedance (Action/Limit Level) of construction noise was recorded in the reporting period.

3.2.3 Water Quality Monitoring

The water quality monitoring results are summarized in **Table 3.4**. Graphical plots of the monitoring data are shown in **Appendix F**. The weather conditions in the reporting period are provided in **Appendix G**.

Table 3.4: Summary of Water Quality Monitoring Results

Monitoring Date	Temp (ºC)	pH	Dissolved Oxygen (DO) (mg/L)	DO (%)	Turbidity (NTU)	BOD (mg/L)[1]	Suspended Solids (mg/L)
MP3							
02/03/2022	19.2	7.4	7.3	87.7	16.7	4	27
04/03/2022	20.3	7.4	7.4	90.8	29.3	5	32
07/03/2022	20.6	7.5	7.4	91.8	30.3	3	39
09/03/2022	23.2	7.5	7.6	89.5	21.2	3	22
11/03/2022	23.7	7.5	7.5	87.9	22.9	3	29
14/03/2022	25.3	7.4	7.7	93.0	29.2	4	49
16/03/2022	26.2	7.5	7.7	98.0	27.3	16	**71**
18/03/2022	26.3	7.4	7.8	97.4	31.1	5	28
21/03/2022	26.6	7.5	7.6	95.2	34.6	7	38
23/03/2022	23.6	7.3	7.5	89.0	26.3	10	26
25/03/2022	23.5	7.4	7.6	90.4	28.9	17	17
28/03/2022	25.2	7.4	7.7	93.0	27.5	15	16
30/03/2022	26.5	7.4	7.6	95.3	18.9	3	16
Action Level	-	<5.5 or >7.5	<6.85	-	>64	-	>65
Limit Level	-	<4.0 or >8.0	<6.65	-	>67	-	>66
MP4							
02/03/2022	19.0	7.2	5.8	75.0	20.1	8	28
04/03/2022	20.0	7.3	5.9	78.4	29.9	5	31
07/03/2022	20.2	7.2	6.0	79.8	38.2	5	**54**
09/03/2022	23.1	7.3	5.8	69.6	22.4	4	24
11/03/2022	23.2	7.3	6.0	69.8	23.1	4	26
14/03/2022	24.9	7.2	5.9	71.9	35.2	5	39
16/03/2022	26.0	7.3	5.8	72.6	33.8	16	**69**
18/03/2022	26.0	7.2	6.0	74.6	34.5	6	32
21/03/2022	26.3	7.2	6.1	76.3	36.2	7	40
23/03/2022	23.3	7.1	6.0	70.4	32.4	12	26
25/03/2022	23.4	7.2	6.0	70.2	33.2	3	20
28/03/2022	25.0	7.0	6.1	74.3	32.1	17	25
30/03/2022	26.3	7.2	6.0	74.0	36.5	<2	38
Action Level	-	<5.5 or >7.5	<3.91	-	>60	-	>50
Limit Level	-	<4.0 or >8.0	<3.82	-	>64	-	>53
MP5							
02/03/2022	19.4	7.0	5.6	69.6	32.4	10	35
04/03/2022	20.5	7.1	5.6	70.9	38.1	6	40
07/03/2022	20.5	7.1	5.7	74.1	43.0	6	40
09/03/2022	23.4	7.1	5.5	66.5	30.3	4	35
11/03/2022	23.5	7.1	5.7	67.4	37.2	6	40
14/03/2022	25.4	7.3	6.0	73.5	42.8	6	41

Monitoring Date	Temp (ºC)	pH	Dissolved Oxygen (DO) (mg/L)	DO (%)	Turbidity (NTU)	BOD (mg/L)(1)	Suspended Solids (mg/L)
16/03/2022	26.5	7.2	5.6	69.4	38.4	21	59
18/03/2022	26.4	7.3	5.7	70.0	37.8	6	30
21/03/2022	26.5	7.3	5.8	72.4	39.9	4	27
23/03/2022	23.9	7.0	5.9	69.6	35.4	5	31
25/03/2022	23.7	7.1	5.8	67.9	44.5	4	32
28/03/2022	25.4	7.2	5.8	71.7	36.8	17	22
30/03/2022	26.6	7.0	5.8	72.0	40.3	9	37
Action Level	-	<5.5 or >7.5	<4.13	-	>81	-	>66
Limit Level	-	<4.0 or >8.0	<3.87	-	>84	-	>69
MP6							
02/03/2022	19.6	7.0	5.5	68.1	39.3	10	38
04/03/2022	20.4	7.1	5.5	69.0	47.7	7	62
07/03/2022	20.6	7.1	5.6	71.7	46.5	8	49
09/03/2022	23.7	7.1	5.6	67.9	41.1	6	46
11/03/2022	24.0	7.2	5.5	64.9	40.8	7	42
14/03/2022	25.6	7.3	5.7	69.4	43.6	5	46
16/03/2022	26.6	7.2	5.4	66.3	44.6	18	48
18/03/2022	26.4	7.3	5.5	67.9	41.8	7	33
21/03/2022	26.6	7.3	5.6	70.5	43.3	13	37
23/03/2022	24.0	7.1	5.7	68.3	36.6	10	29
25/03/2022	23.9	7.1	5.5	65.2	46.6	16	41
28/03/2022	25.5	7.1	5.6	69.4	39.1	16	28
30/03/2022	26.7	7.1	5.5	69.7	44.3	7	37
Action Level	-	<5.5 or >7.5	<4.61	-	>94	-	>75
Limit Level	-	<4.0 or >8.0	<4.52	-	>96	-	>75

Notes:
(1) "<2": Value is too low to indicate (<2mg/L).
(2) Values in **Bold** indicate Action Level exceedance.
(3) Values **Underlined and in Bold** indicate Limit Level exceedance.

3.2.3.1 Exceedance Investigation and Findings

During March 2022, three Limit Level exceedances of SS were observed. One Limit Level exceedance of SS was recorded at MP3 and two Limit Level exceedances of SS were recorded at MP4.

Exceedance of SS at MP3

Exceedance of the Limit Level of SS was observed on 16 March 2022 at MP3.

As understood, the fish pond near the site (represented by MP3) is separated from the open ditch by the pond bund (since commencement of construction phase EM&A monitoring in May 2010) and from the construction site by the WRA (since it was completed in November 2010). No direct discharge from the project site to the fish pond was observed.

Mitigation measures for water quality protection, including the provision of wastewater treatment facilities (including sedimentation tank and AquaSed) and proper drainage system that separates from the WRA, have been implemented. No adverse impact on the fish pond near the site was observed, including on the day with exceedance of water quality parameters.

On the day of SS exceedance, the water body was observed to be a slightly muddy in appearance at MP3 with some floating litter (See Photo 1 which follows). It is noted that SS exceedance was also detected at MP4 on the same date, where floating litter and dead leaves were observed (see Photo 2).

It is concluded that the exceedance of SS at MP3 was possibly due to localised natural variations and external factors such as litter and pond fish culture activities in the fish pond represented by MP3, which are not related to project construction activities.

Exceedances of SS at MP4

Exceedance of the Limit Level of SS was observed on 7 and 16 March 2022 at MP4.

The Hong Kong Observatory (HKO) records indicate that up to 10mm of rainfall were recorded at the project site on 7 March 2022. The rainfall may have caused surface runoff from all sources near the open ditch. It is believed that the runoff increased the turbulence and thus resulted in higher SS inside the ditch water on 7 March 2022, when SS exceedance was recorded.

Also, on the days of SS exceedances, the water body at MP4 was observed to be slightly muddy, with water plant growth, floating dead leaves and litter (see Photos 2 and 3). An increased amount of water plant growth was observed on 16 March 2022, resulting on a particularly high BOD level recorded at MP4. SS levels were also high at MP5 and MP6 on the days of the SS exceedances at MP4, although no exceedances were recorded upstream.

As presented in the weekly site inspections checklists, no observation regarding discharge of muddy water was recorded in March 2022. It is possible that the water plant growth and litter may have impeded the normal flow of ditch water resulting in localised accumulations of SS.

It is concluded that the exceedances of SS at MP4 were possibly due to localised natural variations and external factors such as rainfall, water plant growth, floating dead leaves and litter, which are not related to project construction activities.

Photo 1 **Appearance of the water body at MP3 on 16 March 2022**

Photo 2 **Appearance of the water body at MP4 on 16 March 2022**

Photo 3 **Appearance of the water body at MP4 on 7 March 2022**

4 Ecological Monitoring

4.1 Monitoring of Birds

This report documents surveys conducted in the Survey Area between 1 and 31 March 2022. The Wetland Restoration Area (WRA) is also surveyed as the area is accessible and site formation works for WRA has been completed. The updated survey transect is provided in **Figure 4.1**. Dates and ecological surveys conducted during this period are summarised in **Appendix H**.

Monitoring was undertaken following the survey methodology in the EM&A Manual. A transect was followed in the bird surveys (see **Figure 4.1**). All bird species were identified to species and all bird species of conservation importance and/or wetland dependent were enumerated and recorded to the habitats in which they were observed. Flying birds were not recorded unless they were foraging and/or associated with the habitat (such as swifts, swallows and birds of prey). Further, notable bird observations during other surveys or site inspections were also recorded.

Bird surveys were conducted on a weekly basis. A total of 61 bird species were recorded in the Survey Area (excluding the WRA), 32 of which were species of conservation importance and/or wetland-dependence. Within the WRA, 57 bird species were recorded, 26 of which were species of conservation importance and/or wetland-dependence including two of the three target species (Little Egret and Chinese Pond Heron).

The WRA continues to attract a number of species of conservation importance, including Little Grebe (*Tachybaptus ruficollis*), Great Cormorant (*Phalacrocorax carbo*), Grey Heron (*Ardea cinerea*), Great Egret (*Ardea alba*), Little Egret (*Egretta garzetta*), Chinese Pond Heron (*Ardeola bacchus*), Great Bittern (*Botaurus stellaris*), Black-crowned Night Heron (*Nycticorax nycticorax*), Black Kite (*Milvus migrans*), Wood Sandpiper (*Tringa glareola*), Pacific Swift (*Apus pacificus*), Pied Kingfisher (*Ceryle rudis*), White-throated Kingfisher (*Halcyon smyrnensis*), Chinese Penduline-Tit (*Remiz consobrinus*) and Collared Crow (*Corvus torquatus*). Little Grebe, Black-crowned Night Heron, Wood Sandpiper, Pacific Swift, Pied Kingfisher, White-throated Kingfisher and Collared Crow are listed by Fellowes *et al*. as of “Local Concern” in 2002. Great Cormorant, Grey Heron, Great Egret, Little Egret and Chinese Pond Heron are listed by Fellowes *et al*. as of “Potential Regional Concern” in 2002. Great Bittern, Black Kite and Chinese Penduline-Tit are listed by Fellowes *et al*. as of “Regional Concern” in 2002.

A summary of survey data is provided in **Appendix I**.

4.2 Monitoring of Herpetofauna

One daytime and one night-time herpetofauna surveys were scheduled in the reporting month. Three amphibian species and one reptile species were recorded in the Survey Area (excluding the WRA) during regular surveys. Within the WRA, three amphibian species and three reptile species were recorded during regular surveys.

A summary of the survey findings is provided in **Appendix J**.

4.3 Monitoring of Dragonflies and Butterflies

One odonates and butterflies survey was scheduled in the reporting month. Four odonate species and seven butterfly species were recorded in the Survey Area (excluding the WRA) during regular surveys. Within the WRA, twelve odonate species and 16 butterfly species were recorded during regular surveys. Four odonate species were recorded outside regular surveys, within the WRA,

of which three were also recorded during regular surveys. Among the odonate species recorded within the WRA, Blue Sprite (Pseudagrion microcephalum) is listed by Fellowes et al. as of "Local Concern" in 2002.

A summary of the survey findings is provided in **Appendix J**.

4.4 Monitoring of Mammals

Monitoring of mammals was conducted concurrently with other faunal surveys. Any mammal species encountered during site inspections or other habitat management works were recorded as 'outside survey'.

Two mammal species (Short-nosed Fruit Bat *Cynopterus sphinx* and Japanese Pipistrelle *Pipistrellus abramus*) were recorded in both the Survey Area (excluding the WRA) and within the WRA during regular surveys.

A summary of the survey findings is provided in **Appendix J**.

4.5 Monitoring of Water Quality

Since the water level reached its action level in February 2022, monitoring effort were doubled in March 2022. Regular water level monitoring was conducted on 15 March 2022, and additional water level monitoring was conducted on 29 March 2022. The water levels in the reporting month ranged between 165 and 210cm during the water level monitoring works.

The water level of the Cells allowed wetland birds to use them as foraging sites and attracted diving birds such as Little Grebe (*Tachybaptus ruficollis*) and Great Cormorant (*Phalacrocorax carbo*) to forage. The shallower areas along the edges of ponds and islets attracted ardeids such as Grey Heron (*Ardea cinerea*), Great Egret (*Ardea alba*), as well as the target species Little Egret (*Egretta garzetta*) and Chinese Pond Heron (*Ardeola bacchus*). These areas were also used by many wetland-dependent birds as foraging and/or perching sites, such as the Common Kingfisher (*Alcedo atthis*) and White-throated Kingfisher (*Halcyon symrnensis*). The current water level will be kept for wetland bird usage.

In-situ water quality monitoring of all other parameters was conducted on 22 March 2022.

Monitoring data is presented in **Appendix K**. Locations for the monitoring of water quality for the ecological monitoring are shown in **Figure 4.2**.

4.6 Management Activities

4.6.1 Vegetation Management

Vegetation management activities undertaken at the site primarily involved removal of excess grass and broken branches. Weeding works were conducted along the emergency vehicular access (EVA) and pond bunds of Cell 1 and Cell 2. Excessive branches of Cell 3 and Cell 4 were swept aside, forming piles of plant materials on both sides of the EVA. These piles were used to attract herpetofauna.

Long grass and reeds along the pond bunds were used by passerines such as Plain Prinia (*Prinia inorata*) and Yellow-bellied Prinia (*Prinia flaviventris*) as breeding sites. Current weeding works aimed at maintaining the accessibility of survey transect. Breeding progress of the birds will be closely monitored during bird surveys and site inspection works, before conducting further management works of the grass and reeds.

Reed-dependent Purple Heron (*Ardea cinerea*) was recorded regularly within the WRA over the last few months. The presence of the bird species will be closely monitored before conducting any management work of reeds within the WRA.

Wetland dependent Little Grebe (*Tachybaptus ruficollis*), Common Moorhen (*Gallinula chloropus*) and White-breasted Waterhen (*Amaurornis phoenicurus*) were seen collecting nesting materials and foraging along the islets in the Cells, as well as along the edges of the pond bunds. Breeding progress of this species will be closely monitored before conducting any management work of vegetation within the WRA.

4.6.2 Wildlife Management

Red Imported Fire Ant nests along the cell bunds and along the EVA were checked and marked. Nests along the EVA will be treated with approved pesticide in the coming months.

Egg masses of the Apple Snails (*Pomacea canaliculate)* found along the concrete structures of the WRA (e.g. sluice gates between Cells, and concrete wall of Cell 4) were cleared. Egg masses found on vegetation along the islets and Cell edges will be cleared after close monitoring of the breeding status of wetland-dependent birds in the following months.

Mitigation actions have been taken in the WRA during the survey period to increase the WRA utilization by birds, including:

1. Controlling the vegetation at Cell 1, Cell 2, Cell 3 and Cell 4; and
2. Controlling the water level at Cell 1, Cell 2, Cell 3 and Cell 4.

4.7 Summary

Ecological monitoring during March 2022 was carried out according to the survey methodology and frequency outlined in the EM&A Manual.

A summary of the survey findings is listed in **Table 4.1**:

Table 4.1: Summary of Ecological Monitoring in WRA and Survey Area under EM&A Manual

Species	Survey Area (excluding WRA)	WRA
Birds (total)	61	57
Birds (of conservation importance and/or wetland-dependence)	32	26
Amphibians	3	3
Reptiles	1	3
Mammals	2	2
Odonates	4	12
Butterflies	7	16

Survey findings indicate that the ponds within the Survey Area supported numbers and diversity of wetland-dependent birds typical of fishpond areas. The WRA continues to attract wetland dependent fauna and serves as a buffer between the residential portion and the fishponds in the north.

Dense and tall vegetation along the edge of the EVA attracted migratory insectivorous birds such as Daurian Redstart (*Phoenicurus auroreus*), Dusky Warbler (*Phylloscopus fuscatus*) and Yellow-browed Warbler (*Phylloscopus inornatus*). Breeding attempts of passerines such as Light-vented Bulbul (*Pycnonotus sinensis*), Red-whiskered Bulbul (*Pycnonotus jocosus*), Oriental Magpie

Robin (*Copsychus saularis*), Cinereous Tit (*Parus cinereus*), Swinhoe's White-eye (*Zosterops simplex*), Masked Laughingthrush (*Garrulax perspicillatus*), Common Tailorbird (*Orthotomus sutorius*) and Black-collared Starling (*Gracupica nigricollis*) were observed among the vegetations (e.g. territorial call, display, collection of nesting materials, etc.). These vegetations were also be used by butterflies and odonates as perching sites. The vegetation stands will be kept as long as the branches do not overgrow and obscure the EVA. During the vegetation clearance some of these environments were treated only with minimum trimming to preserve suitable habitats for the wildlife.

The reedbed of the WRA attracted several migratory insectivorous birds such as Dusky Warbler (*Phylloscopus fuscatus*) and Stejneger's Stonechat (*Saxicola stejnegeri)*. The reedbed will be closely monitored before conducting any clearance work.

Fallen leaves scattered along the EVA were swept aside and formed a thicker layer of fallen plant materials. These piled-up plant materials are used to attract amphibians and reptiles within the WRA in the warmer and wetter months.

During the herpetofauna night-time survey on 29 March 2022, one male Rimmed Window Firefly (*Pyrocoelia analis*) was recorded in the reed along the edge of Cell 1. Although fireflies were not included in the monitoring work, these wetland dependent insects would also indicate the quality of the WRA. This group will be recorded when encountered during surveys of other taxa.

5 Landscape and Visual

5.1 Site Inspections

The EM&A programme for Landscape and Visual impact due to the construction commenced in June 2010 and continued during the reporting period. Site inspections on Landscape and Visual impact were carried out on 11 and 25 March 2022 to confirm the implementation of mitigation measures at the construction stage.

The Event and Action Plan for Landscape & Visual is shown in **Appendix D**.

5.2 Construction Phase Audit Summary

The audit was undertaken with reference to the specific checklists provided in **Table 2.13 – Table 2.15** and audit results are summarized below in **Table 5.1**. Representative photos showing the implementation of mitigation measures are presented in **Appendix M**.

Table 5.1: Construction and Operation Phase Audit Summary

Area of Works	Items of be Monitored
Works Area	The boundaries of the works area have been established on site in accordance with the contract documents and approved plans (EP), and the limit of current heavy construction activity is now confined to within the site hoardings (North side of the site / access road) and the noise barriers (other sides of the site). Minor works such as horticultural maintenance of the planting and transplanted trees, and boundary fence repair was proceeding along the Royal Palms – Palm Springs boundary. (**Appendix M** Photo 1 – **Table 2.14** CM2 refers) No construction works were observed to have exceeded the site boundaries. No construction was carried out at the wetland restoration area after 15 November 2010.
Protection of all trees and woodland blocks to be retained	Trees retained within the site along the northeast boundary, beside wetland restoration area, have been identified and protected by temporary protective fencing.
Streams	The works site is partly encircled by a berm / perimeter channel to intercept surface water and prevent it from washing off into any of the neighbouring sites. Surface water is collected within the site in a temporary drainage channel. Gravels beds and barriers have been installed to filter site runoff, sedimentation ponds have been provided to enable primary treatment before discharge to mains drains.
Clearance of existing vegetation	Site clearance was completed prior to the commencement of construction.
Transplanting of trees	Tree transplanting has been completed, with the trees relocated to various points within the planting strip along the southern boundary of the site, outside the noise barrier. Most of the trees continue to re-establish well.
Topsoil stripping	Suitable pond bund and soil material which had been excavated and stockpiled from the original site, has now been re-used within the landscape works. Dust suppression measures are active along all internal site access tracks.
New buildings	No new permanent buildings have yet been constructed on site.
Boundaries	Hoardings have been erected along most of the boundaries of the site. Installation of new screen fence between the future residential sites and the constructed wetland restoration areas is complete. Fence has been painted green to match with the surrounding vegetated environment. (**Appendix M** Photo 1 – **Table 2.14** CM2 refers)
Noise Barrier	Noise barriers have been installed along the southern and western boundaries of the site in accordance with the contract requirements. Their design complies with the mitigation requirements, with upper 6 to 7m portion of the barrier being made from a translucent material with green tinted (to match with the environment). Supporting GMS structure, likewise, has been painted green. (**Appendix M** Photo 3 – **Table 2.14** CM6 refers).
Night-time lighting	No night-time works were reported to have been carried out during the monitoring period.

Area of Works	Items of be Monitored
Landscape and wetland treatments generally	Continuous belt of screen planting along the southern and western boundaries of the site has been completed. The formation, soiling and water control structures of the wetland restoration area have been completed. (**Appendix M** Photo 3 – **Table 2.14** CM6 refers) The wetland areas are being established, with the ponds are being seasonally filled with rainwater. Planting of areas around the WRA cells is complete. No construction was carried out at the wetland restoration area after 15 November 2010. (**Appendix M** Photo 2 – **Table 2.14** CM2 refers)
Soiling, etc.	The soil placement and grading for each of the wetland restoration areas has been completed. Refilling for those holes left after the whole tree removal works has been completed.
Plant supply	The plant material used in the Advance Planting Strip and in the WRA are all commonly available species and came from commercial sources. Transplanted reeds (*Phragmites australis*) at the wetland habitat came from the temporary holding nursery onsite.
Planting	The tree species are all from the approved list. Seedling trees and shrubs have been established at the margins of the wetland cells. Some invasive species and undesirable exotic species have been found during site inspection, removal of these species should be undertaken on a regular basis.
Establishment Works	The advance planting, the compensatory planting and transplanted trees are generally being maintained by the landscape sub-contractor in accordance with the specification to ensure that the contract requirements are met. Removal of overgrown weeds, unplanned tree seedlings and invasive climbers in the space behind screen noise barrier needs to be undertaken on a monthly basis as they may inhibit the advance planting. Red imported fire ant (RIFA) nests were observed along the maintenance path of the WRA area. A sign of RIFA spreading throughout the WRA area was observed. To avoid water contamination, it is recommended to keep monitoring for the spread of RIFA nests during the wet seasons. Eradication of all the nests should be undertaken in the earlier part of the dry seasons. Regular removal of invasive species (i.e. apple snails, *Leucaena leucocephala, Mikania micrantha, Mimosa pudica, Bidens alba, Ludwigia erecta, Sesbania cannabina*, etc.) in WRA should be undertaken. The growth of shrubs / seedlings on the north side of WRA remains fair.

6 Environmental Site Inspection and Audit

6.1 Site Inspection

The ET had carried out construction phase weekly site inspections on 2, 11, 16 and 25 March 2022. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary. The key observations from site inspections and associated recommendations are summarized in **Table 6.1**.

Table 6.1: Summary of Site Inspections and Recommendations

Key Observations	ET Recommendation	Contractor's Responses / Action(s) Undertaken	Close-out (Date)
Nil			

6.2 Solid and Liquid Waste Management Status

The Contractor has been registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting was carried out on site. A sufficient number of receptacles were available for general refuse collection.

As advised by the Contractor, no inert C&D material (i.e. broken concrete/ big boulders) were generated on site and sent to a sorting facility for recycling into rockfill. No metals were generated and collected by registered recycling collector. No paper/cardboard packing and no plastics were generated on site and collected by registered recycling collector. No chemical waste was generated and collected by licensed chemical waste collector. No other types of wastes (e.g. general refuse) were generated on site and disposed of at public landfill facility.

The Contractor is advised to maintain on site waste sorting and recording system and maximize reuse / recycling of C&D wastes, whenever these are generated.

6.3 Status of Environmental Licences and Permits

The environmental permits, licences, and/or notifications on environmental protection for this Project which were valid during the reporting period is summarised in **Table 6.2**.

Table 6.2: Status of Environmental Submissions, Licences and Permits

Statutory Reference	Description	Permit/Reference No.	Status
EIAO	Environmental Permit	EP-311/2008/E	Valid
APCO	Notification of Construction Work under APCO	2018-027-A-1 (20 July 2020)	Valid
WPCO	Discharge Licence	WT00037436-2021 (21 Apr 2021)	Valid
WDO	Registration as Chemical Waste Producer	WPN0000-542-H3083-04	Valid
WDO	Bill Account for Disposal	700945423	Valid

Legend: EIAO – Environmental Impact Assessment Ordinance; APCO – Air Pollution Control Ordinance; WPCO – Water Pollution Control Ordinance; WDO – Waste Disposal Ordinance

6.4 Recommended Mitigation Measures

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental

mitigation measures are provided in **Appendix L**. In particular, the following mitigation measures were brought to attention during the site audits.

Air Quality

- Dark smoke emission from equipment/plant should be avoided.

Noise

- The noise barriers and hoardings should have no gaps and openings to avoid noise leakage.

Water Quality

- Site effluent should be discharged in accordance with discharge licence.
- The site should be confined and properly maintained to avoid silt runoff.
- Chemicals will always be stored on drip trays or in bunded areas.

Waste Management

- The chemical waste storage area should be clearly labelled.
- General refuse should be stored in enclosed bins or compaction units separate from C&D and chemical wastes.

7 Report on Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions

7.1 Record of non-compliance of Action and Limit Levels

There was no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting month.

During March 2022, three Limit Level exceedances of SS were observed. One Limit Level exceedance of SS was recorded at MP3 and two Limit Level exceedances of SS were recorded at MP4.

A summary is presented in **Table 7.1** below.

Table 7.1: Summary of Exceedances in Water Quality

Monitoring Date	pH	Dissolved Oxygen (DO) (mg/L)	Turbidity (NTU)	Suspended Solids (mg/L)
MP3				
16/03/2022	7.5	7.7	27.3	**<u>71</u>**
Action Level	<5.5 or >7.5	<6.85	>64	>65
Limit Level	<4.0 or >8.0	<6.65	>67	>66
MP4				
07/03/2022	7.2	6.0	38.2	**<u>54</u>**
16/03/2022	7.3	5.8	33.8	**<u>69</u>**
Action Level	<5.5 or >7.5	<3.91	>60	>50
Limit Level	<4.0 or >8.0	<3.82	>64	>53

Notes:
(1) "<2": Value is too low to indicate (<2mg/L).
(2) Values in **Bold** indicate Action Level exceedance.
(3) Values **<u>Underlined and in Bold</u>** indicate Limit Level exceedance.

7.2 Record on Environmental Complaints Received

No environmental complaint was received during the reporting month.

7.3 Record on Notifications of Summons and Successful Prosecution

No notifications of summons or successful prosecution were received the reporting month.

7.4 Review of Reasons for and Implications of Non-compliance, Complaints, Summons and Prosecutions

Non-compliance

Investigations have been carried out to identify the causes of the water quality exceedances.

The investigation findings are presented in **Section 3.2.3.1**. It was concluded that the abovementioned exceedances were unlikely to be due to the construction works and therefore not considered to be related to the project.

Complaints, Summons and Prosecutions

Not applicable for this reporting month.

7.5 Follow-up Actions Taken

Non-compliance

As a non-compliance has been recorded, the Event and Action Plan has been followed. Although it is considered that the exceedances were not related to the Project, the Contractor was reminded to implement the water quality mitigation measures in accordance with the recommendation stated in Section 5.6.1 – 5.6.4 of the EIA Report as far as practicable, regular spot checks would be conducted on the nearby discharge by the Contractor and he would inform the ET for investigation.

Complaints, Summons and Prosecutions

Not applicable for this reporting month.

7.6 Cumulative Statistics for Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics for complaints, notifications of summons and successful prosecutions for the Project account for period starting from the date of commencement of construction (i.e., 12 May 2010) to the end of the reporting month and are summarized in **Table 7.2** below.

Table 7.2: Statistics for Complaints, Notifications of Summons and Successful Prosecution

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of Summons	Successful Prosecutions
This reporting month (March 2022)	0	0	0
From 12 May 2010 to end of the reporting month (March 2022)	8	0	0

8 Future Key Issues

8.1 Site Preparatory Works and Construction Works for the Coming Month

Site works to be commissioned in the coming month include:

- Regular maintenance work for the Wetland Restoration Area (including lowering of the water level and removal of unwanted species in the pond)
- No major construction works

8.2 Key Issues for the Coming Months

Key issues to be considered in the coming three months include:

- Provision of water spraying or dust suppression chemical to prevent generation of dust from activities on-site and the haul road during dry weather conditions;
- Provision of wheel washing facilities at vehicle exit point;
- Generation and treatment of site surface runoffs and wastewater from activities on-site and during wet weather conditions;
- Sorting, recycling, storage and disposal of general refuse and construction waste from activities on-site; and
- Management of chemicals and avoidance of oil spillage on-site and to the drainage system.

8.3 Monitoring Schedule for the Coming Month

The environmental site inspection and environmental monitoring will be continued in the coming month. Impact monitoring for air, noise, water quality, ecology and landscape and visual in accordance with the approved EM&A Manual has commenced since 12 May 2010. The tentative monitoring schedule for April 2022 is shown in the **Table 8.1**.

Table 8.1: Tentative Environmental Monitoring and Audit Schedule for the Next Reporting Month

Environmental Monitoring and Audit Schedule for April 2022

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1 Water * 24-hr TSP 1-hr TSP	2
3	4 Water	5 Ching Ming Festival	6 Water	7 **Bird** 24-hr TSP 1-hr TSP Noise Monitoring	8 Water * **Landscape**	9
10	11 Water	12 **Dragonfly & Butterfly**	13 Water * 24-hr TSP 1-hr TSP Noise Monitoring	14 **Bird** @	15 Good Friday	16 The day following Good Friday
17	18 Easter Monday	19 Water 24-hr TSP 1-hr TSP Noise Monitoring	20 **Water Quality Monitoring**	21 Water **Bird** **Landscape**	22 **Herpetofauna (night-time)** *	23 Water
24	25 Water 24-hr TSP 1-hr TSP Noise Monitoring	26	27 Water **Dragonfly & Butterfly**	28 **Bird** **Herpetofauna (daytime)**	29 Water *	30

* Site Audit by Mott MacDonald (MM)

@ Report Submission (Monthly EM&A Report)

Ecological Surveys & Landscape Audits indicated in **bold font**

8.4 Conclusions and Recommendations

8.4.1 Conclusions

The EM&A programme as recommended in the EM&A manual has been undertaken in the reporting month since 12 May 2010.

Monitoring of Air Quality, Noise, Water Quality, Ecology and Landscape and Visual impacts due to the Project was under way. In particular, the 1-hr TSP, 24-hr TSP, noise level (as L_{eq}) and water quality parameters (such as pH, DO, turbidity and SS) under monitoring have been checked against established Action and Limit levels.

There was no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting month.

During March 2022, three Limit Level exceedances of SS were observed. One Limit Level exceedance of SS was recorded at MP3 and two Limit Level exceedances of SS were recorded at MP4.

8.4.2 Recommendations

With considerations on the construction activities and environment, the following recommendations were provided:

Air Quality

- All stockpiles should be covered by tarpaulin or kept wet by water spraying;
- All vehicles should be washed to remove any dusty materials before leaving the construction sites;
- The portion of road leading the construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;
- During the dry season, sufficient water spraying should be provided at haul road to reduce dust emission; and
- Ensure proper functioning of the wheel wash facility.

Noise

- Mobile plant should be sited as far away from NSRs as possible;
- Plant known to emit noise strongly in one direction should be orientated to direct noise away from the NSRs; and
- The construction activities should be better scheduled to reduce noise nuisance.

Water Quality

- Effluent should be discharged in accordance with the discharge licence conditions;
- Soil contaminated with chemicals/oils should be removed from site and the voids should be created filled with suitable materials; and
- Silt and debris should be removed from the temporary drainage channel regularly.

Waste Management

- General refuse should be stored in enclosed bins or compaction units separate from C&D and chemical wastes to minimise odour, pest and litter impacts.
- Reuse the excavated materials as far as practical to reduce the amount of waste disposal;
- C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal;
- Ensure drip trays are provided for chemical containers to prevent leakage or soil contamination;
- All plants and vehicles should be properly maintained to prevent oil leakage; and
- Oil stains on soil should be cleared by disposal of contaminated soil.

Figures

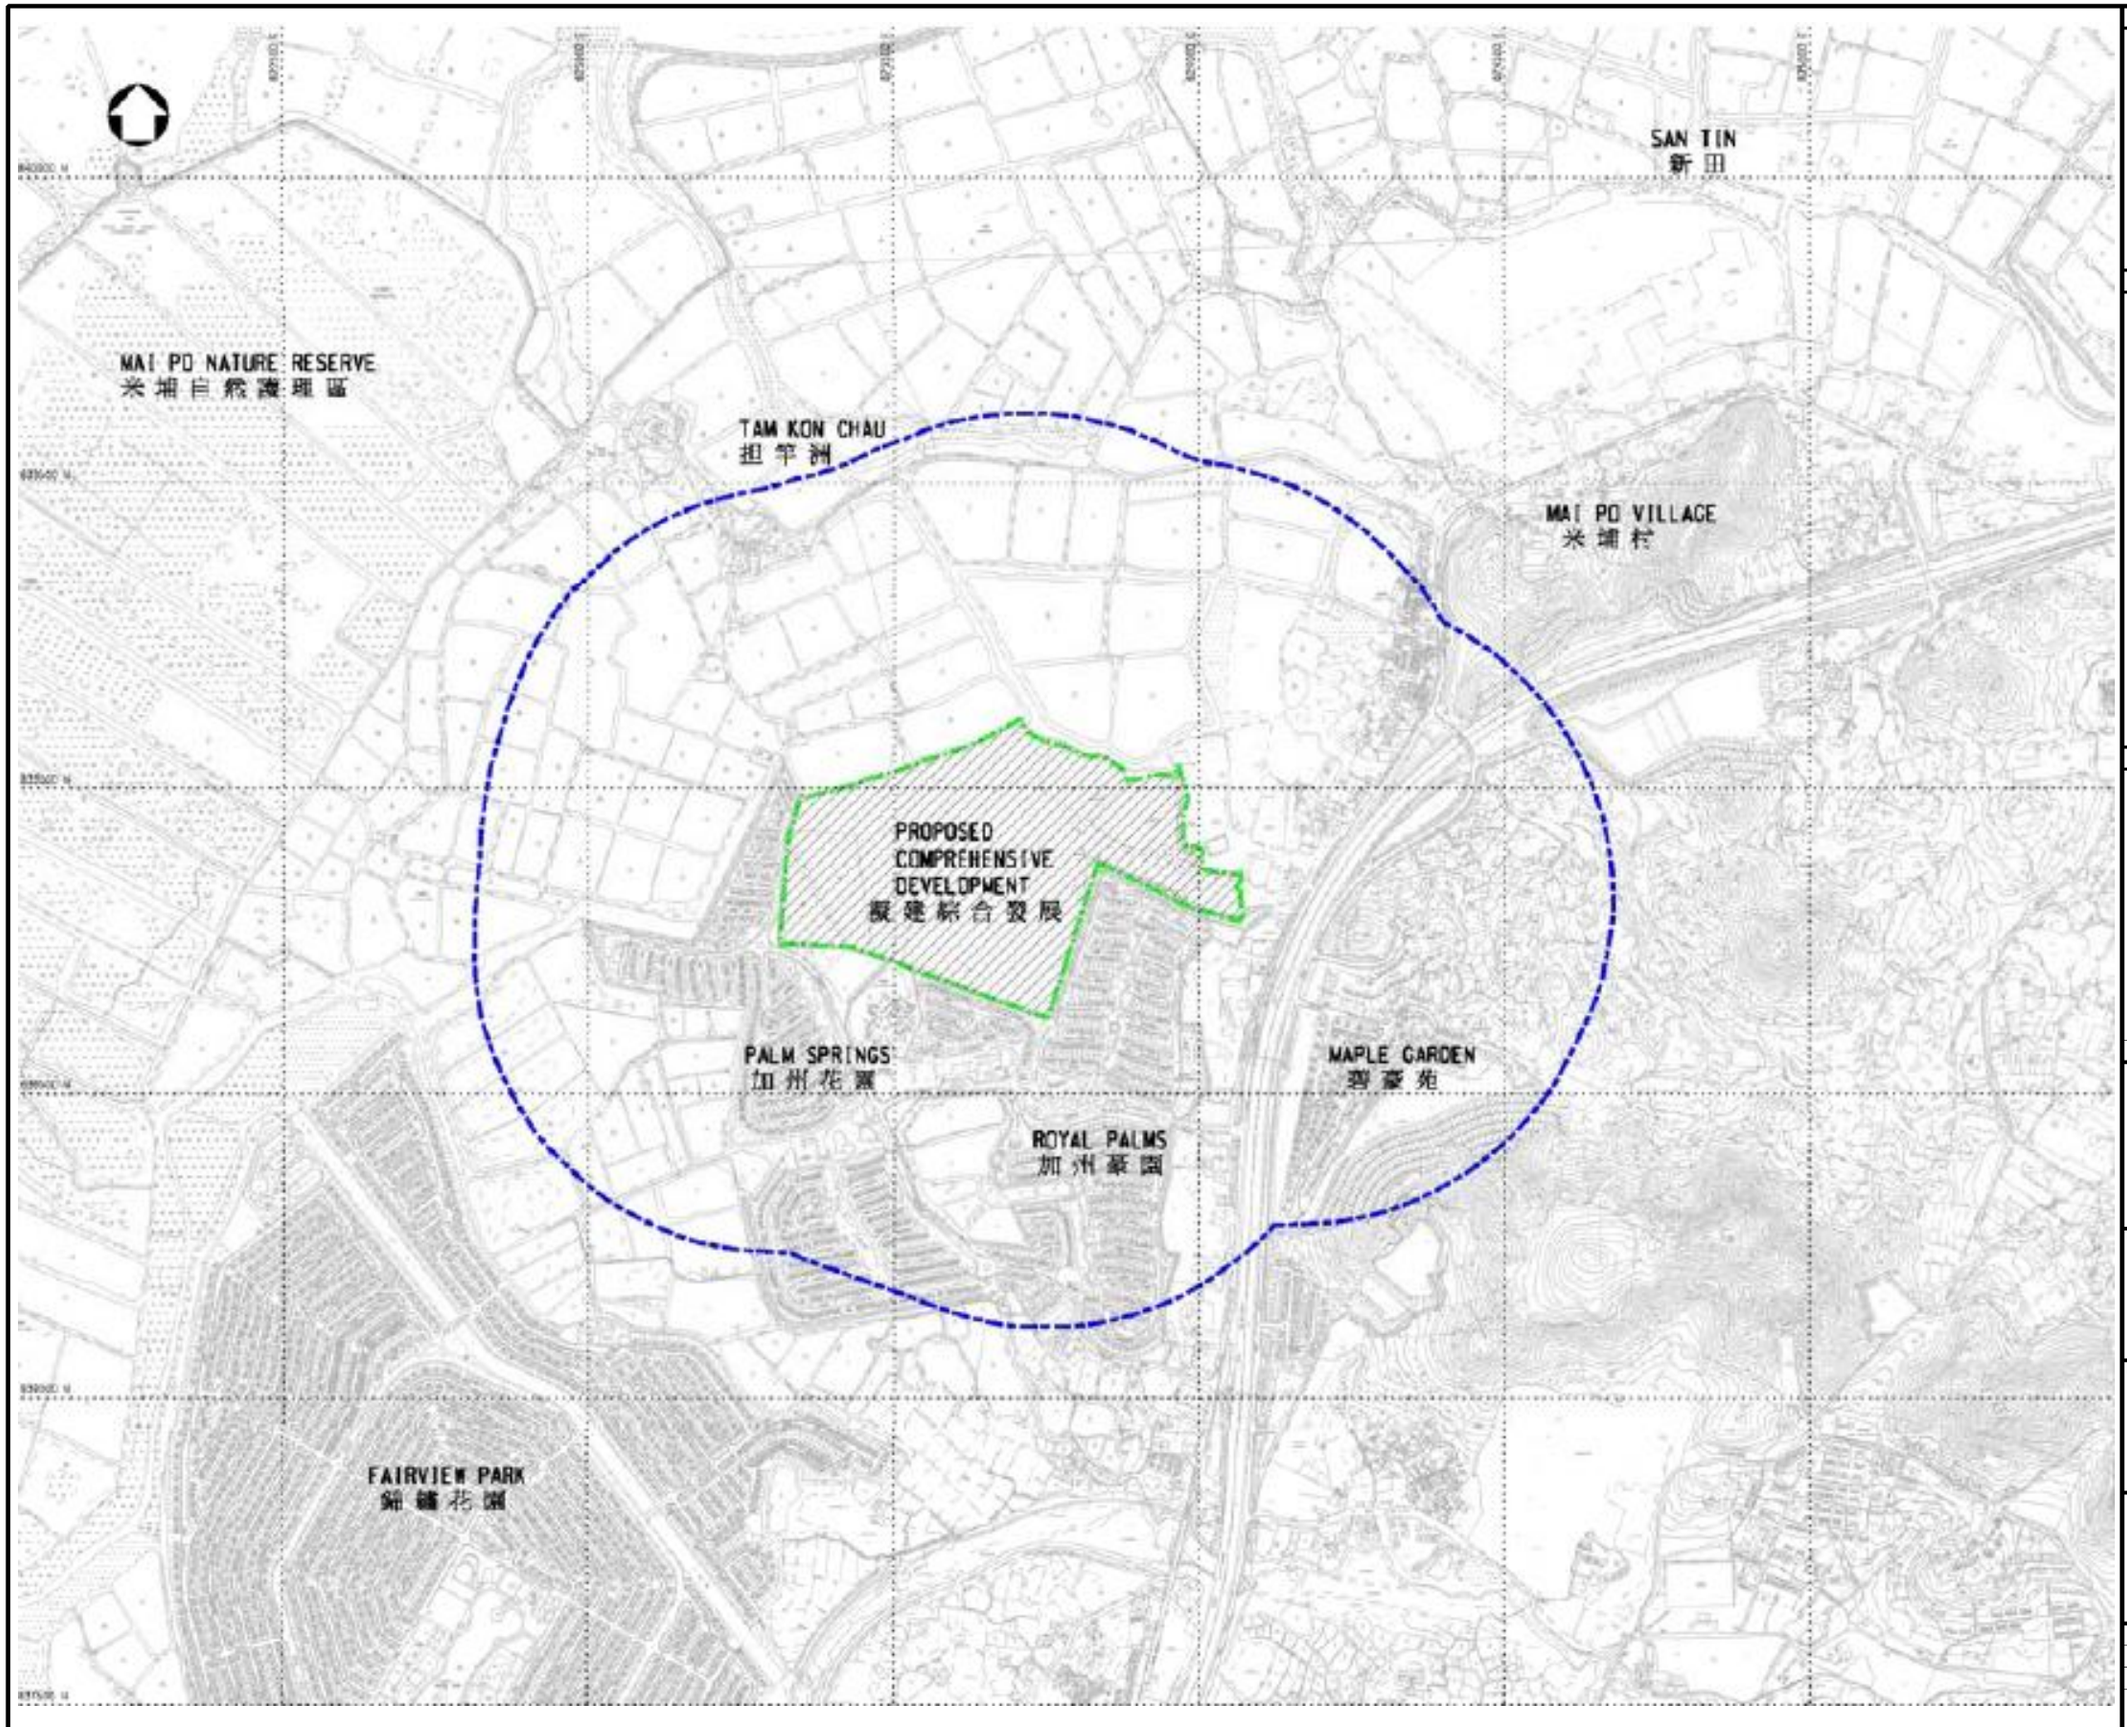

Notes

Key to symbols

Site Boundary

500m Assessment Area

Proposed Comprehensive Development

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd

MOTT MACDONALD

3/F Manulife Place
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

PROFIT POINT ENTERPRISES LIMITED

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

General Layout Plan of the Project Site

Designed			Eng check		
Drawn			Coordination		
Dwg check			Approved		
Scale at A1		Status		Rev	

Drawing Number

Figure 1.1

© Mott MacDonald
This document is issued for the party which commissioned it and for specific purposes connected with the captioned project only. It should not be relied upon by any other party or used for any other purpose.
We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

Notes

Key to symbols

★ Construction Phase Air Quality Monitoring Locations

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd

MOTT MACDONALD

3/F Manulife Place
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

PROFIT POINT ENTERPRISES LIMITED

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

Locations of Air Quality Monitoring Stations

Designed			Eng check		
Drawn			Coordination		
Dwg check			Approved		
Scale at A1		Status		Rev	

Drawing Number

Figure 2.1

© Mott MacDonald
This document is issued for the party which commissioned it and for specific purposes connected with the captioned project only. It should not be relied upon by any other party or used for any other purpose.
We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

F:\425047-Hong Kong\6 0-BIM\02_WIP\01_CV\DRAWING\03_CAD\XREF\MMH-425047-P-A1_TLB-N.dgn DATE: 15/12/2021 TIME: 15:48:46 USER: TSE45790

Notes

Key to symbols

- Construction Phase Noise Monitoring Stations

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd

MOTT MACDONALD

3/F Manulife Place
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

PROFIT POINT ENTERPRISES LIMITED

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

Locations of Noise Monitoring Stations

Designed			Eng check		
Drawn			Coordination		
Dwg check			Approved		
Scale at A1		Status		Rev	

Drawing Number

Figure 2.2

© Mott MacDonald
This document is issued for the party which commissioned it and for specific purposes connected with the captioned project only. It should not be relied upon by any other party or used for any other purpose.
We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

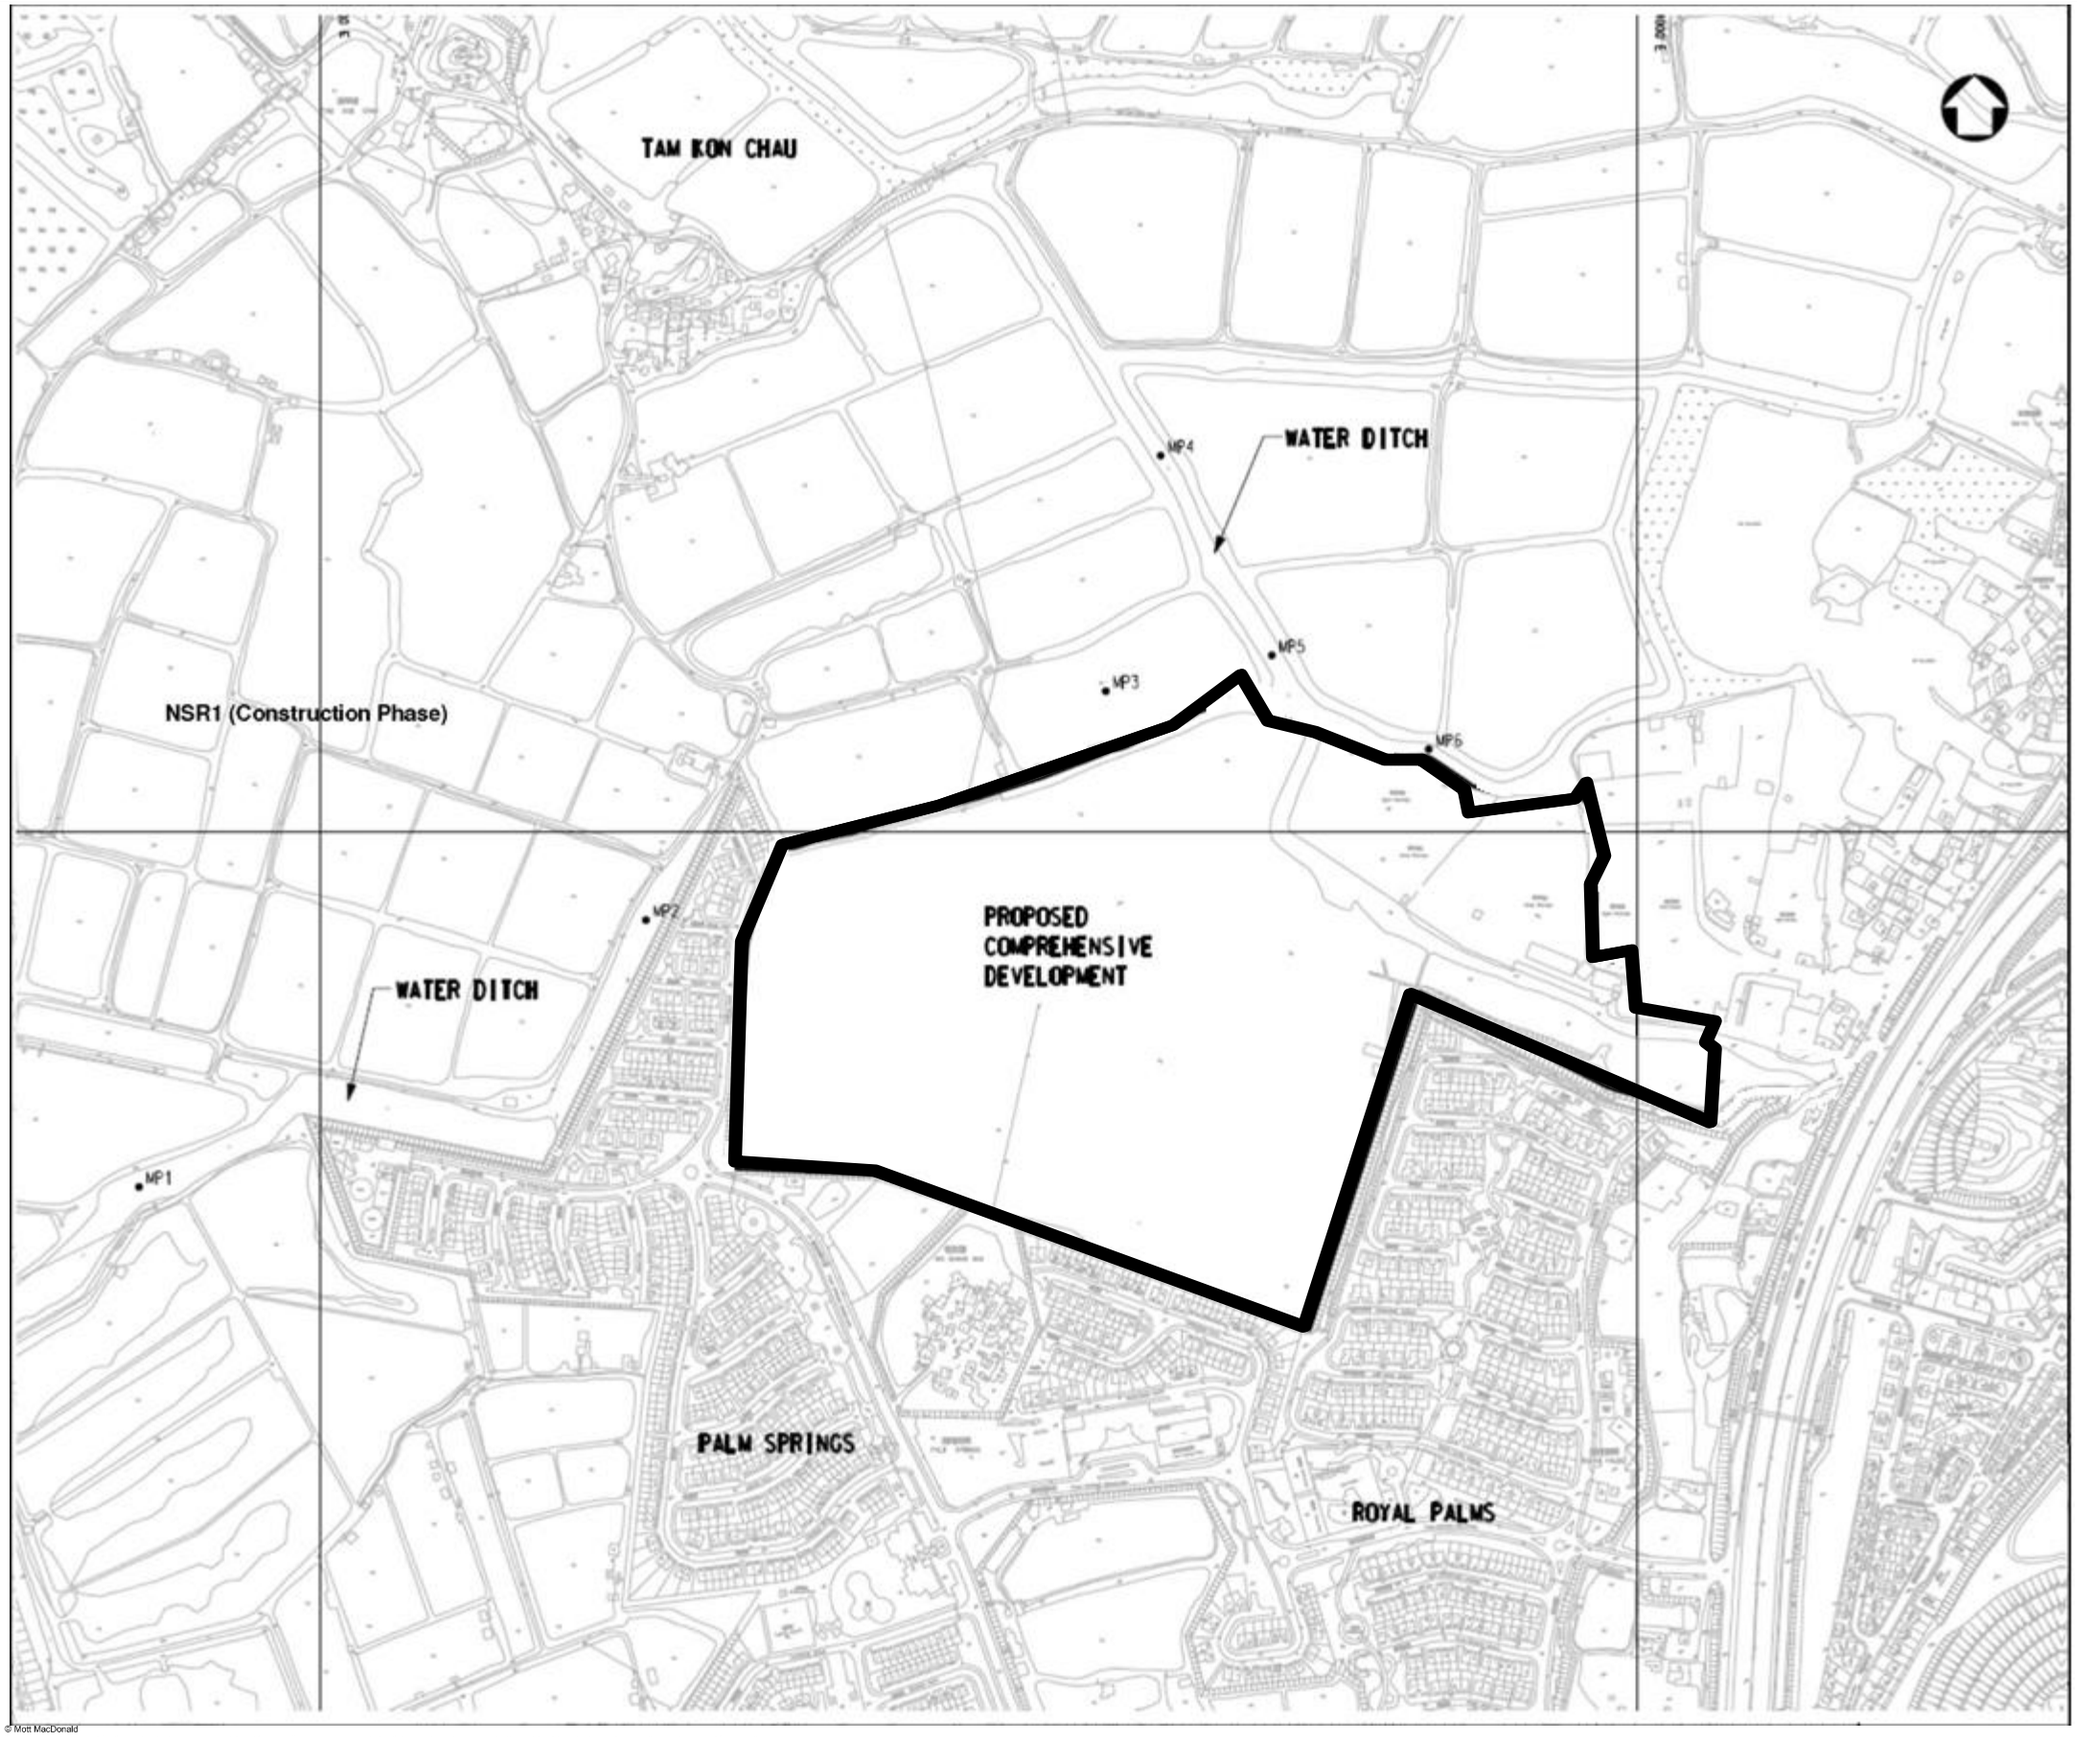

Notes

Key to symbols

- Water Quality Monitoring Stations
- Site Boundary

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd

MOTT MACDONALD

3/F Manulife Place
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

PROFIT POINT ENTERPRISES LIMITED

Project

PROPOSED COMPREHENSIVE DEVELOPMENT
AT WO SHANG WAI, YUEN LONG

Title

Locations of Water Quality Monitoring Stations

Designed			Eng check		
Drawn			Coordination		
Dwg check			Approved		
Scale at A1		Status		Rev	

Drawing Number

Figure 2.3

© Mott MacDonald
This document is issued for the party which commissioned it and for specific purposes connected with the captioned project only. It should not be relied upon by any other party or used for any other purpose.
We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

F:\425047-Hong Kong\6.0-BIM\02_WIP\01_CV\DRAWING\03_CAD\XREF\MMH-425047-P-A1_TLB-N.dgn DATE:15/12/2021 TIME:15:48:46 USER:TSE45790

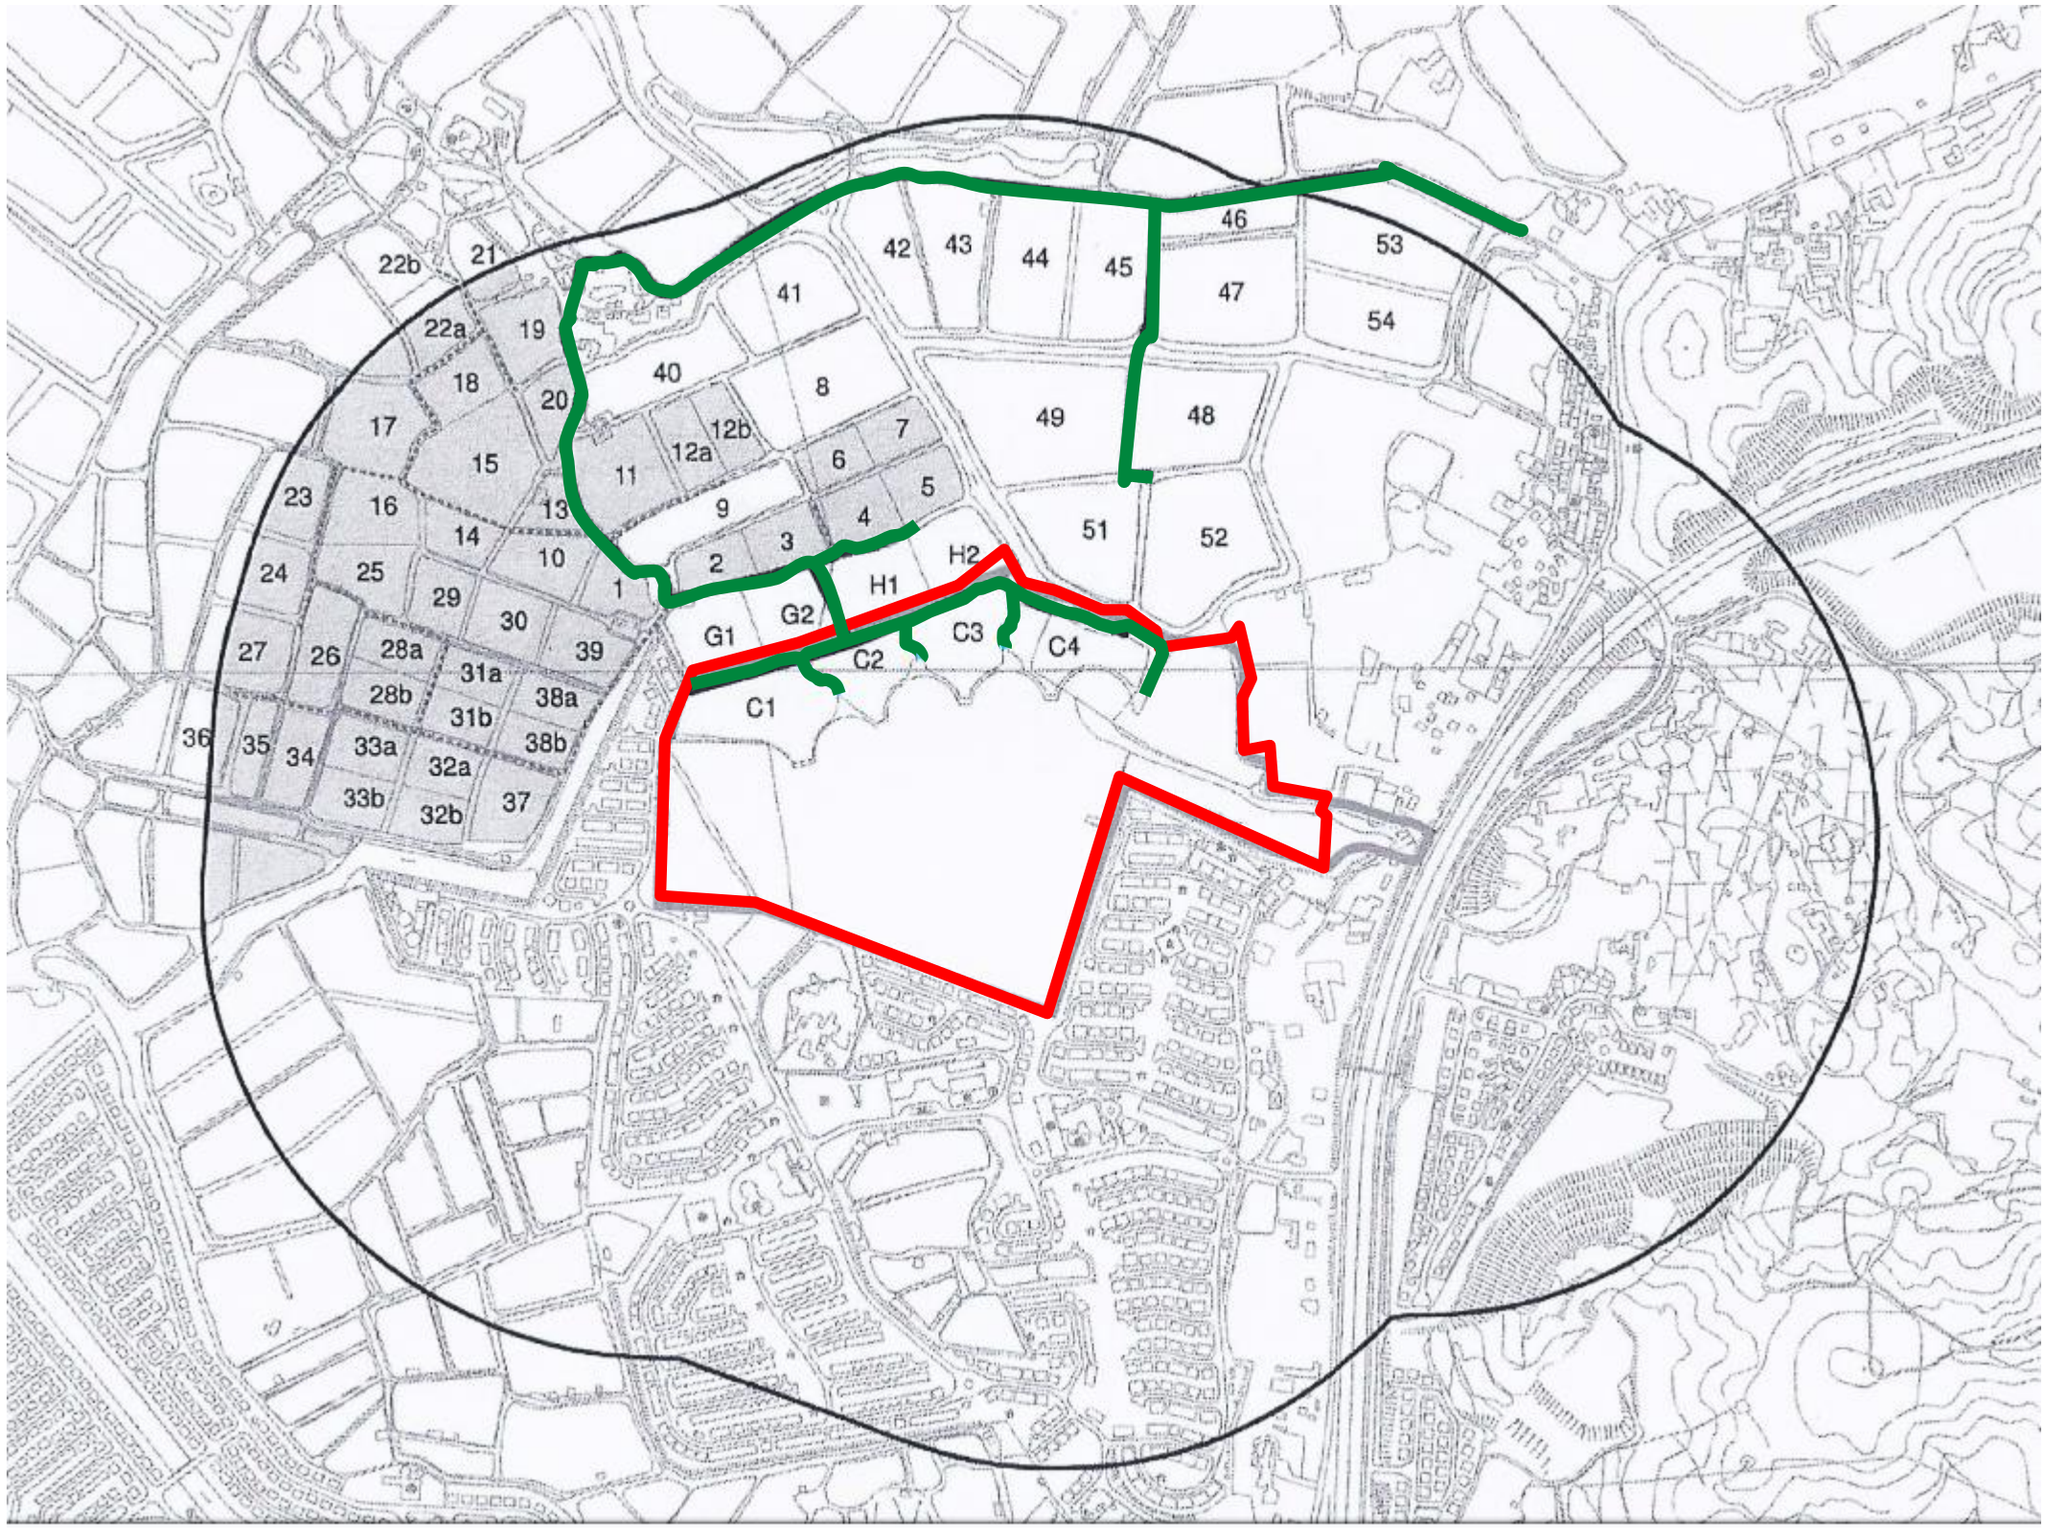

Notes

Key to symbols

Project Area

Assessment Area

Transect

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd

MOTT MACDONALD

3/F Manulife Place
348 Kwun Tong Road
Kwun Tong, Kowloon
Hong Kong
T +852 2828 5757
F +852 2827 1823
W mottmac.com

Client

PROFIT POINT ENTERPRISES LIMITED

Project

PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI, YUEN LONG

Title

Survey Area and Transect Walked

Designed			Eng check		
Drawn			Coordination		
Dwg check			Approved		
Scale at A1		Status		Rev	

Drawing Number

Figure 4.1

© Mott MacDonald
This document is issued for the party which commissioned it and for specific purposes connected with the captioned project only. It should not be relied upon by any other party or used for any other purpose.
We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

F:\425047-Hong Kong\6 0-BIM\02_WIP\01_CV\DRAWING\03_CAD\XREF\MMH-425047-P-A1_TLB-N.dgn DATE: 15/12/2021 TIME: 15:48:46 USER: TSE45790

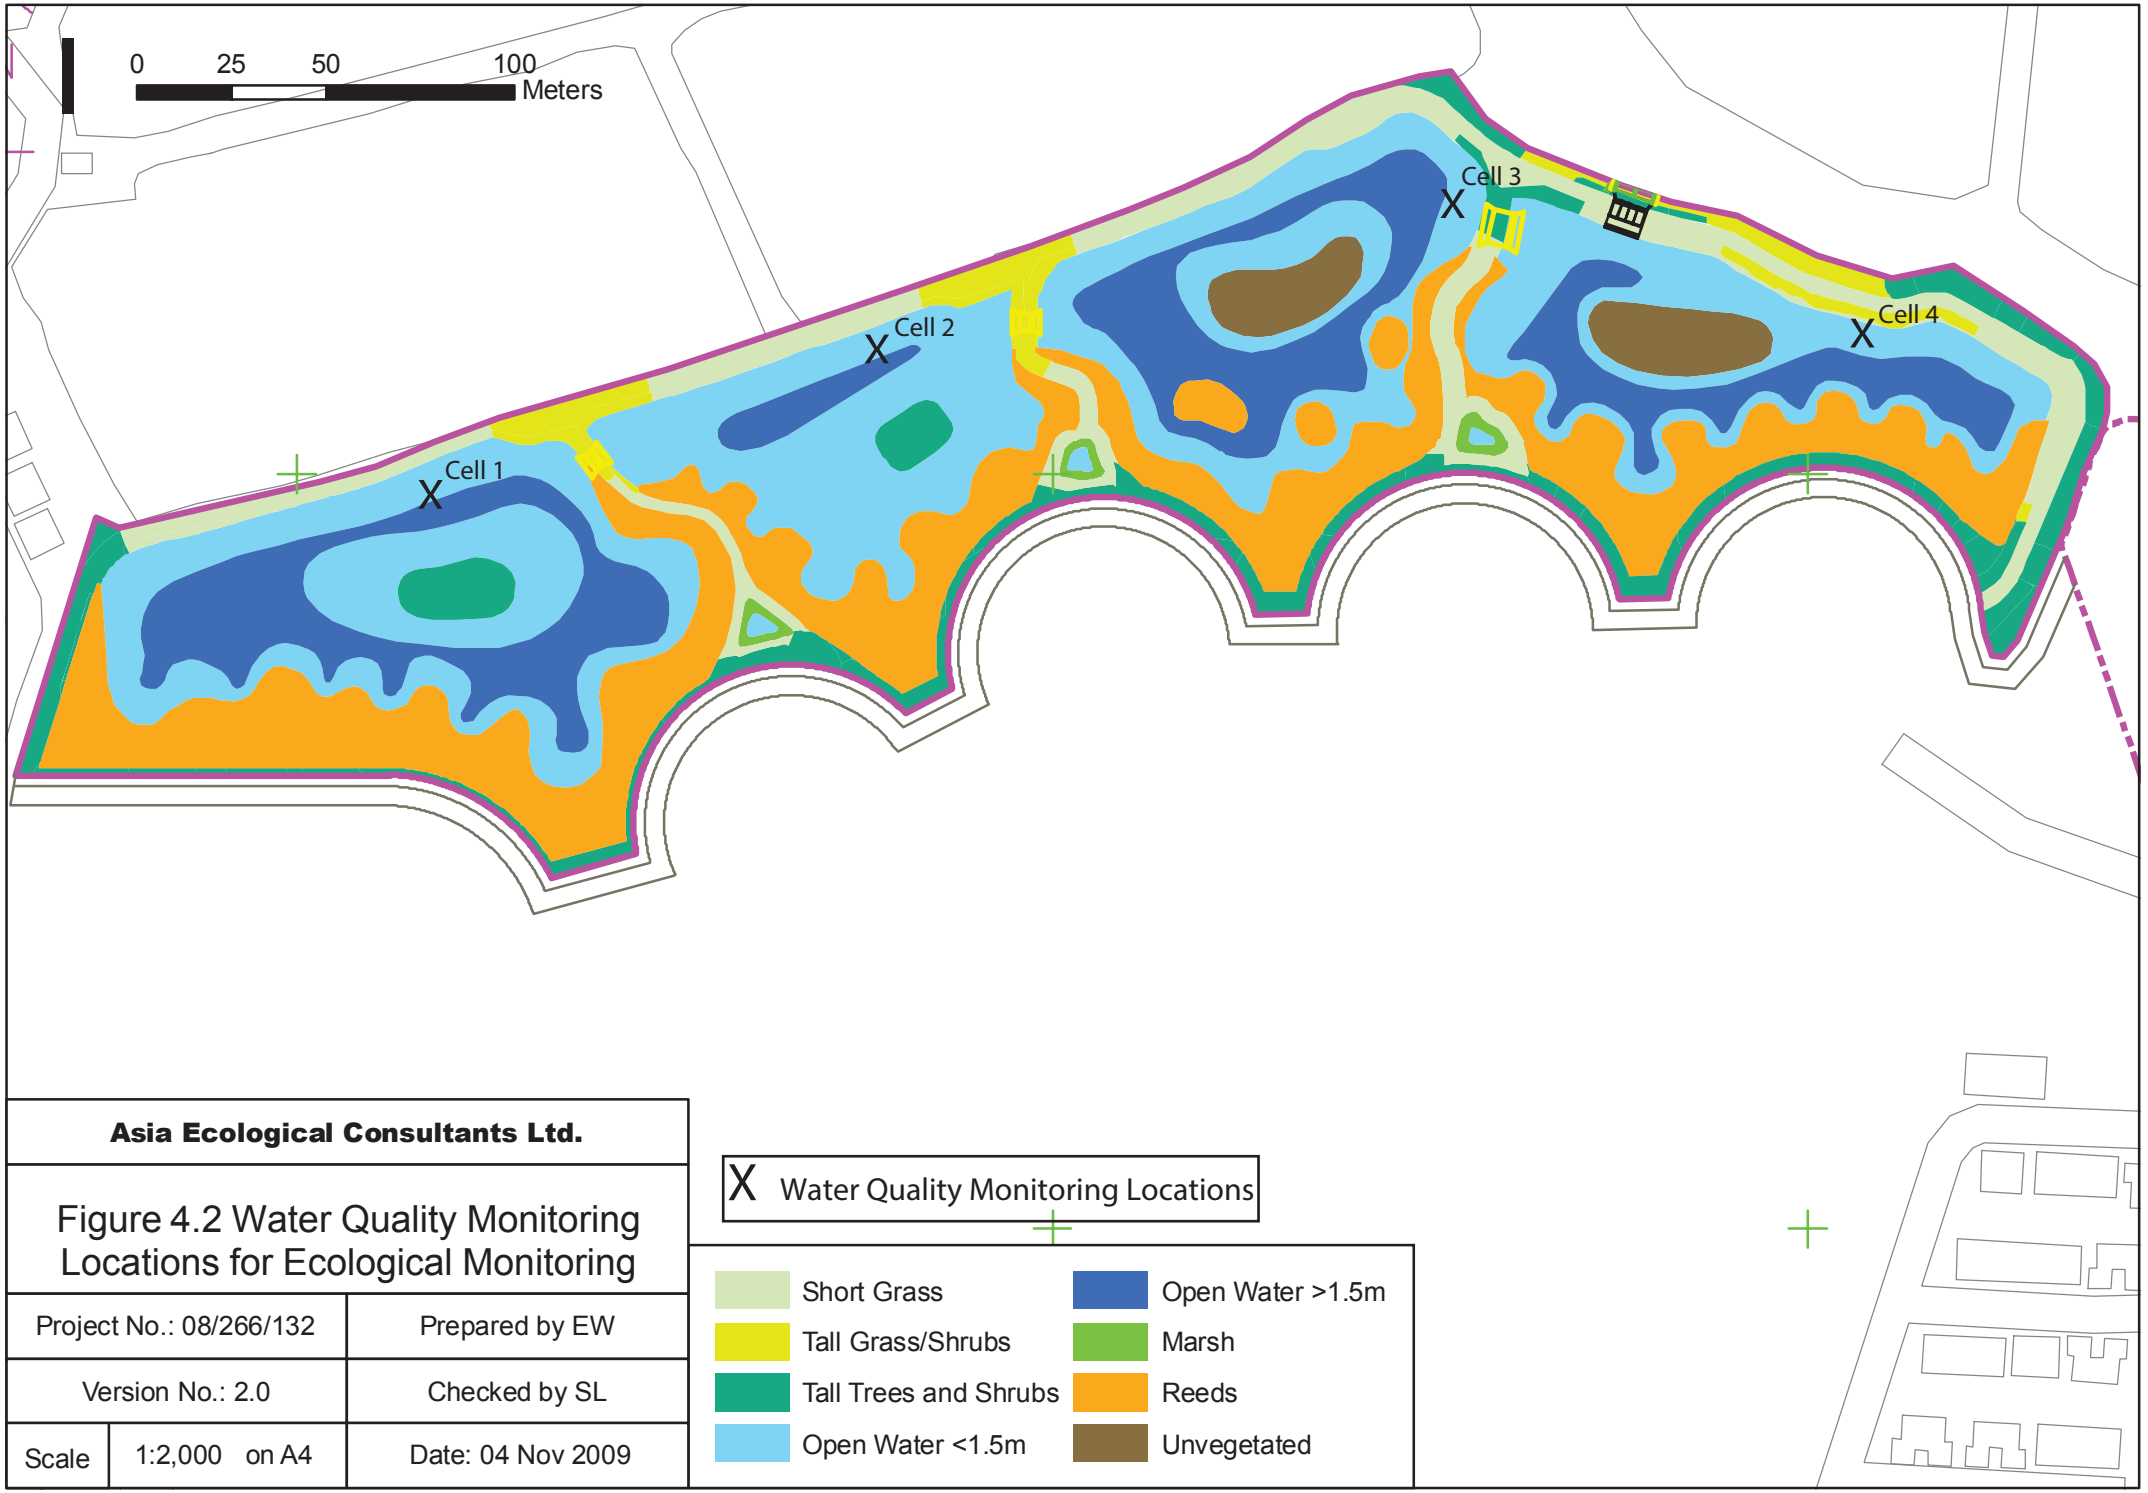

Asia Ecological Consultants Ltd.

Figure 4.2 Water Quality Monitoring Locations for Ecological Monitoring

Project No.: 08/266/132	Prepared by EW
Version No.: 2.0	Checked by SL
Scale 1:2,000 on A4	Date: 04 Nov 2009

Appendices

A.	Project Organization Chart	41
B.	Tentative Construction Programme (not used)	43
C.	Action and Limit Levels for Construction Phase	45
D.	Event and Action Plan for Air Quality, Noise, Water Quality and Landscape & Visual	47
E.	Calibration Certificates	53
F.	Graphical Plots of the Monitoring Results	55
G.	Weather Conditions during the Monitoring Period	57
H.	Ecological Monitoring conducted	59
I.	Summary of Bird Surveys conducted	61
J.	Summary of Herpetofauna, Mammal and Insect Surveys conducted	67
K.	Summary of Water Quality Monitoring associated with Ecological Monitoring conducted	71
L.	Environmental Mitigation Measures - Implementation Status	73
M.	Landscape and Visual Audit Photos	79

A. Project Organization Chart

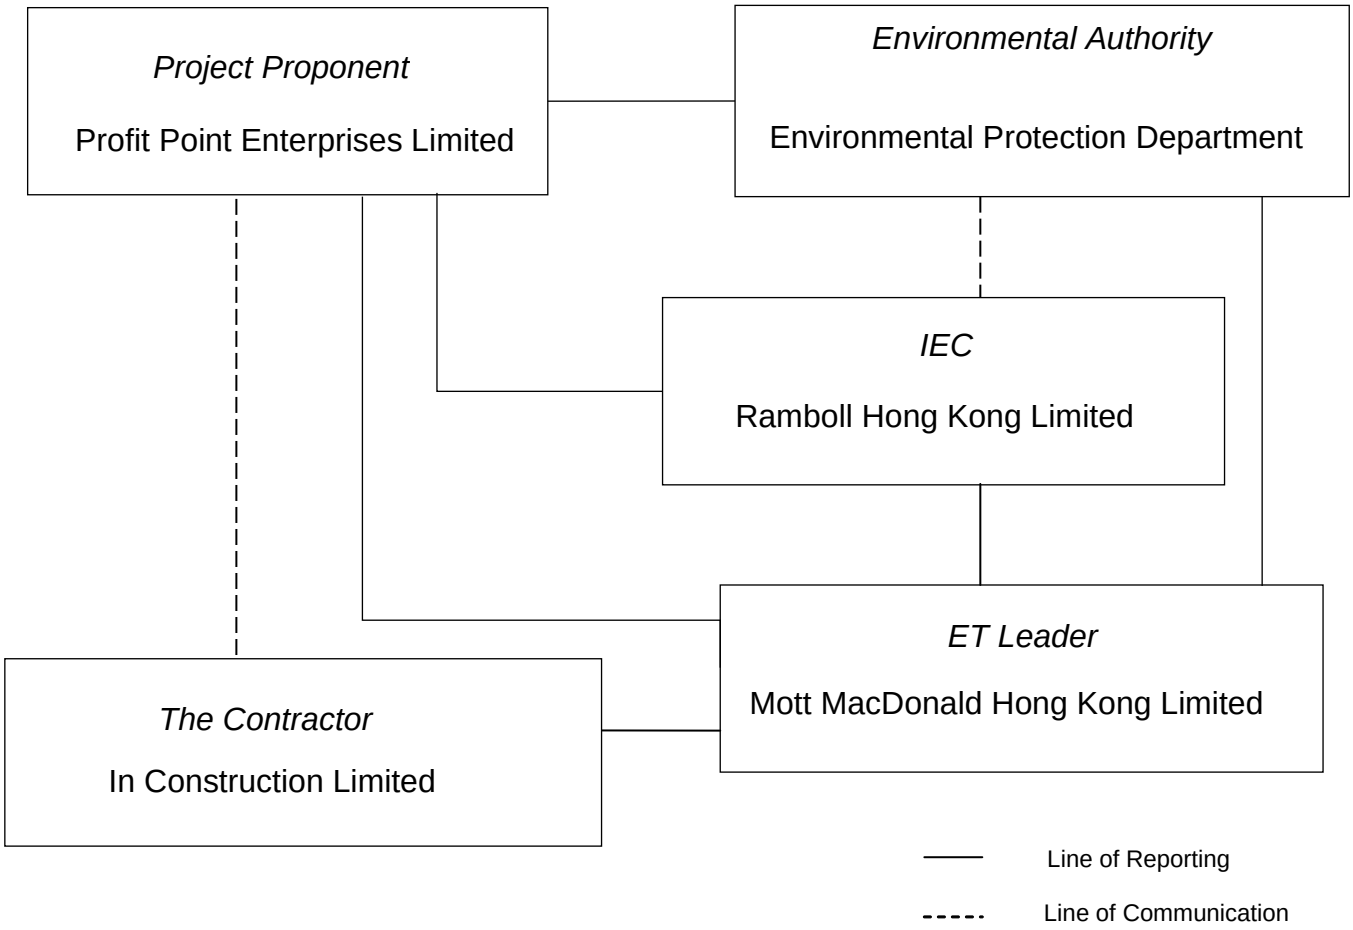

Contact information:

Company	Position	Name	Telephone
Profit Point Enterprises Limited (Project Proponent)	Project Manager	Ms. Stacey Lau	2281 0112
In Construction Limited (The Main Contractor)	Construction Manager	Mr. Chun Kit Tse	9400 7007
	Site Agent	Mr. Chi Hei Leung	6775 1468
	Safety Officer	Mr. Wong Kam Leung	2710 8663
	Environment Officer	Mr. Vega T. L. Wong	6113 2368
Ramboll Hong Kong Limited (Independent Environmental Checker (IEC))	Independent Environmental Checker	Mr. David Yeung	3465 2888
Mott MacDonald Hong Kong Ltd. (Environmental Team (ET))	Environmental Team Leader	Ms. Eugenne Yuen	2828 5998

B. Tentative Construction Programme (not used)

C. Action and Limit Levels for Construction Phase

Air Quality

Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level (μg/m^3)	Limit Level (μg/m^3)
ASR1	226	260
ASR2A	213	260
ASR3	205	260
ASR4	237	260

Action and Limit Levels for 1-hour TSP

Monitoring Station	Action Level (μg/m^3)	Limit Level (μg/m^3)
ASR1	378	500
ASR2A	357	500
ASR3	358	500
ASR4	372	500

Noise

Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
NSR1, NSR3, NSR5, NSR7		
0700 – 1900 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75 dB(A)

Water Quality

Action and Limit Levels for Water Quality

Parameters	DO in mg/L		Turbidity in NTU		SS in mg/L		pH	
	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level	Action Level	Limit Level
MP1	1.23	1.17	173	177	231	299	< 5.5 or > 7.5	< 4.0 or > 8.0
MP2	1.04	0.89	132	163	170	209		
MP3	6.85	6.65	64	67	65	66		
MP4	3.91	3.82	60	64	50	53		
MP5	4.13	3.87	81	84	66	69		
MP6	4.61	4.52	94	96	75	75		

D. Event and Action Plan for Air Quality, Noise, Water Quality and Landscape & Visual

Air Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures. 2. Inform IEC and ER. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET. 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice. 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify the source. 2. Inform IEC and ER. 3. Advise ER on the effectiveness of the proposed remedial measures 4. Repeat measurements to confirm findings. 5. Increase monitoring frequency to daily. 6. Discuss with IEC and the Contractor on remedial actions required. 7. If exceedance continues, arrange meeting with IEC and ER. 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET. 2. Check the Contractor's working method. 3. Discuss with ET Leader and the Contractor on possible remedial measures. 4. Advise ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial actions to IEC within 3 working days of notification. 2. Implement the agreed proposals. 3. Amend proposal if appropriate.

Limit Level				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures. 2. Inform ER and EPD. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET. 2. Check the Contractor's working method. 3. Discuss with ET Leader and the Contractor on possible remedial measures. 4. Advise ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, EPD and the Contractor. 2. Identify the source. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. 6. Arrange meeting IEC and ER to discuss the remedial actions to be taken. 7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary and advise ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. In consultation with IEC, agree with the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by ER until the exceedance is abated.

Construction Noise

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level	1. Notify IEC and the Contractor. 2. Carry out investigation. 3. Report the results of investigation to IEC and the Contractor. 4. Discuss with the Contractor and formulate remedial measures. 5. Increase monitoring frequency to check mitigation measures.	1. Review with analysed results submitted by ET. 2. Review the proposed remedial measures by the Contractor and advise ER accordingly. 3. Supervise the implement of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals to IEC. 2. Implement noise mitigation proposals.
Limit Level	1. Identify the source. 2. Notify IEC, ER, EPD and the Contractor. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency. 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented. 6. Inform IEC, ER, and EPD the causes & actions taken for the exceedances. 7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analysed noise problem. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the ER until the exceedance is abated.

Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level				
1. Exceedance for one sample	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; and 6. Repeat measurement on next day of exceedance.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; and 2. Make agreement on the mitigation measures to be implemented.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER; and 6. Implement the agreed mitigation measures.
2. Exceedance for two or more consecutive samples	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; and 8. Repeat measurement on next day of exceedance.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; and 6. Implement the agreed mitigation measures.

Limit Level				
1. Exceedance for one sample	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; and 7. Increase the monitoring frequency to daily until no exceedance of Limit level.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; and 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; and 4. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days; and 6. Implement the agreed mitigation measures.
2. Exceedance for two or more consecutive samples	1. Repeat in-situ measurement to confirm finding; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; and 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; and 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; and 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures; and 7. As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities.

Landscape and Visual

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level				
Non-conformity on one occasion	1. Identify Source; 2. Inform the IEC and the ER; 3. Discuss remedial actions with the IEC, the ER and the Contractor; and 4. Monitor remedial actions until rectification has been completed.	1. Check report; 2. Check the Contractor's working method; 3. Discuss with the ES and the contractor on possible remedial measures; 4. Advise the ER on effectiveness of proposed remedial measures; and 5. Check implementation of remedial measures.	1. Notify Contractor; and 2. Ensure remedial measures are properly implemented	1. Amend working methods; and 2. Rectify damage and undertake any necessary replacement
Repeated Non-conformity	1. Identify Source; 2. Inform the Project Proponent, IEC and the ER. If serious non-compliance inform EPD; 3. Increase monitoring frequency; 4. Discuss remedial actions with the IEC, the ER and the Contractor; 5. Monitor remedial actions until rectification has been completed; and 6. If exceedance stops, cease additional monitoring.	1. Check monitoring report; 2. Check the Contractor's working method; 3. Discuss with the ES and the Contractor on possible remedial measures; 4. Advise the ER on effectiveness of proposed remedial measures; and 5. Supervise implementation of remedial measures.	1. Notify the Contractor; and 2. Ensure remedial measures are properly implemented.	1. Amend working methods; and 2. Rectify damage and undertake any necessary replacement.

E. Calibration Certificates

Appendix E

Calibration Record

(Air Quality Monitoring)

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: **HK2115630**
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 20-APR-2021
		DATE OF ISSUE	: 3-MAY-2021
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories	*Position*
Richard Fung	Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group
11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK2115630
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ----

ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2115630-001	S/N: 1Y5546	Equipments	20-Apr-2021	S/N: 1Y5546

Equipment Verification Report (TSP)

Equipment Calibrated:

Type:	Laser Dust monitor
Manufacturer:	Sibata LD-3B
Serial No.	1Y5546
Equipment Ref:	Nil
Job Order	HK2115630

Standard Equipment:

Standard Equipment:	Higher Volume Sampler (TSP)
Location & Location ID:	AUES office (calibration room)
Equipment Ref:	HVS 018
Last Calibration Date:	26 April 2021

Equipment Verification Results:

Verification Date: 26 April 2021

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01min	09:11 ~ 11:12	23.4	1013.7	0.026	3004	24.9
2hr	11:16 ~ 13:16	23.4	1013.7	0.027	3135	26.1
2hr01min	13:20 ~ 15:20	23.4	1013.7	0.033	3489	28.9

Linear Regression of Y or X

Slope (K-factor):	0.0011
Correlation Coefficient	0.9966
Date of Issue	30 April 2021

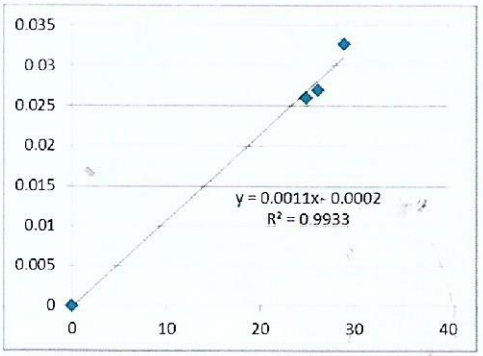

Remarks:

1. **Strong** Correlation (R>0.8)
2. Factor 0.0011 should be applied for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : Date : 30 April 2021

QC Reviewer : Ben Tam Signature : Date : 30 April 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration:	26-Apr-21
Location ID :	Calibration Room	Next Calibration Date:	26-Jul-21

CONDITIONS

Sea Level Pressure (hPa)	1013.7	Corrected Pressure (mm Hg)	760.275
Temperature (°C)	23.4	Temperature (K)	296

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.10574
Model->	5025A	Qstd Intercept ->	-0.00985
Calibration Date->	19-Jan-21	Expiry Date->	18-Jan-22

CALIBRATION

Plate No.	H20 (L) (in)	H2O (R) (in)	H20 (in)	Qstd (m3/min)	I (chart)	IC corrected
18	6.9	6.9	13.8	1.774	56	56.16
13	5.5	5.5	11.0	1.584	50	50.14
10	4.2	4.2	8.4	1.385	42	42.12
8	2.7	2.7	5.4	1.111	32	32.09
5	1.9	1.9	3.8	0.933	22	22.06

LINEAR REGRESSION

Slope = 39.9922
Intercept = -13.7742
Corr. coeff. = 0.9961

Calculations :

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate
IC = corrected chart respones
I = actual chart response
m = calibrator Qstd slope
b = calibrator Qstd intercept
Ta = actual temperature during calibration (deg K)
Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope
b = sampler intercept
I = chart response
Tav = daily average temperature
Pav = daily average pressure

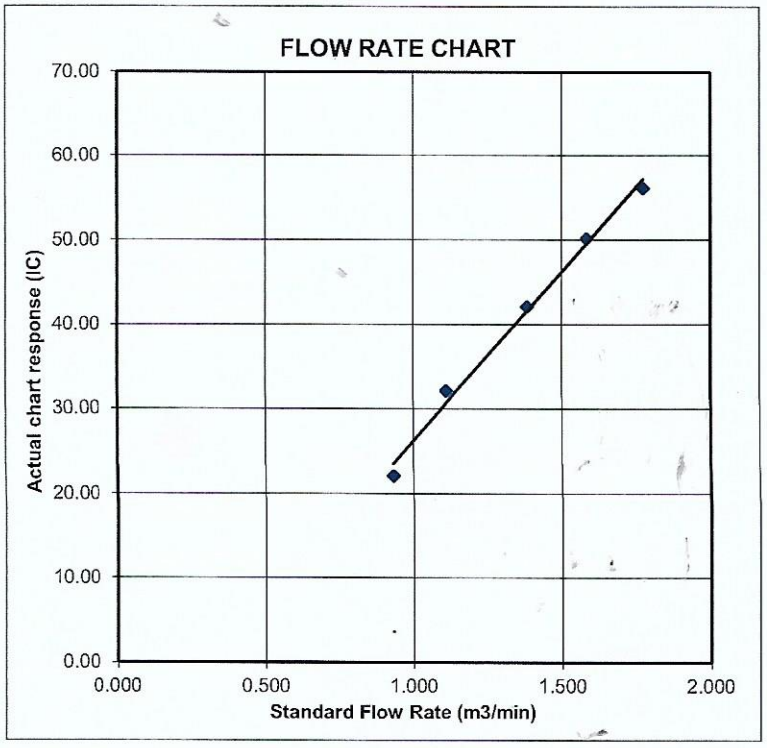

TISCH Environmental

RECALIBRATION DUE DATE:
January 19, 2022

Certificate of Calibration

Calibration Certification Information				
Cal. Date:	January 19, 2021	Rootsmeter S/N: 438320	Ta: 294	°K
Operator:	Jim Tisch		Pa: 755.1	mm Hg
Calibration Model #:	TE-5025A	Calibrator S/N: **1941**		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0420	6.4	4.00
3	5	6	1	0.9290	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7340	12.9	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H\left(Ta/Pa\right)}$ (y-axis)
1.0029	0.6762	1.4192	0.9958	0.6715	0.8824
0.9986	0.9583	2.0071	0.9915	0.9516	1.2479
0.9965	1.0726	2.2440	0.9894	1.0650	1.3952
0.9954	1.1260	2.3535	0.9883	1.1180	1.4633
0.9899	1.3487	2.8385	0.9829	1.3391	1.7648
QSTD	**m=**	**2.10574**	**QA**	**m=**	**1.31858**
	b=	**-0.00985**		**b=**	**-0.00612**
	r=	**0.99992**		**r=**	**0.99992**

Calculations			
Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	**Va=**	ΔVol((Pa-ΔP)/Pa)
Qstd=	Vstd/ΔTime	**Qa=**	Va/ΔTime
For subsequent flow rate calculations:			
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	**Qa=**	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
145 South Miami Avenue
Village of Cleves, OH 45002

www.tisch-env.com
TOLL FREE: (877)263-7610
FAX: (513)467-9009

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: **HK2115633**
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 20-APR-2021
		DATE OF ISSUE	: 3-MAY-2021
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ---

General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories	*Position*
Richard Fung	Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group
11/F, Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK2115633
SUB-BATCH : 1
CLIENT : ENVIROTECH SERVICES CO.
PROJECT : ----

ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2115633-001	S/N: 456666	Equipments	20-Apr-2021	S/N: 456666

Equipment Verification Report (TSP)

Equipment Calibrated:

Type:	Laser Dust monitor
Manufacturer:	Sibata LD-3B
Serial No.	456666
Equipment Ref:	Nil
Job Order	HK2115633

Standard Equipment:

Standard Equipment:	Higher Volume Sampler (TSP)
Location & Location ID:	AUES office (calibration room)
Equipment Ref:	HVS 018
Last Calibration Date:	26 April 2021

Equipment Verification Results:

Verification Date: 26 April 2021

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m^3 (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr01min	09:11 ~ 11:12	23.4	1013.7	0.026	3005	24.9
2hr	11:16 ~ 13:16	23.4	1013.7	0.027	3165	26.4
2hr01min	13:20 ~ 15:20	23.4	1013.7	0.033	3497	29.0

Linear Regression of Y or X

Slope (K-factor): 0.0012

Correlation Coefficient 0.9965

Date of Issue 30 April 2021

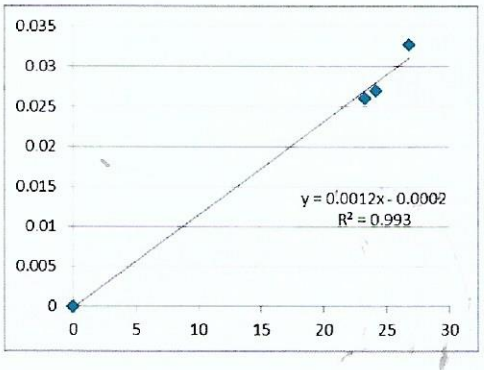

Remarks:

1. **Strong** Correlation (R>0.8)
2. Factor 0.0012 should be applied for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : Date : 30 April 2021

QC Reviewer : Ben Tam Signature : Date : 30 April 2021

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration:	26-Apr-21
Location ID :	Calibration Room	Next Calibration Date:	26-Jul-21

CONDITIONS

Sea Level Pressure (hPa)	1013.7	Corrected Pressure (mm Hg)	760.275
Temperature (°C)	23.4	Temperature (K)	296

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.10574
Model->	5025A	Qstd Intercept ->	-0.00985
Calibration Date->	19-Jan-21	Expiry Date->	18-Jan-22

CALIBRATION

Plate No.	H20 (L) (in)	H2O (R) (in)	H20 (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.9	6.9	13.8	1.774	56	56.16	Slope = 39.9922
13	5.5	5.5	11.0	1.584	50	50.14	Intercept = -13.7742
10	4.2	4.2	8.4	1.385	42	42.12	Corr. coeff. = 0.9961
8	2.7	2.7	5.4	1.111	32	32.09	
5	1.9	1.9	3.8	0.933	22	22.06	

Calculations :

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

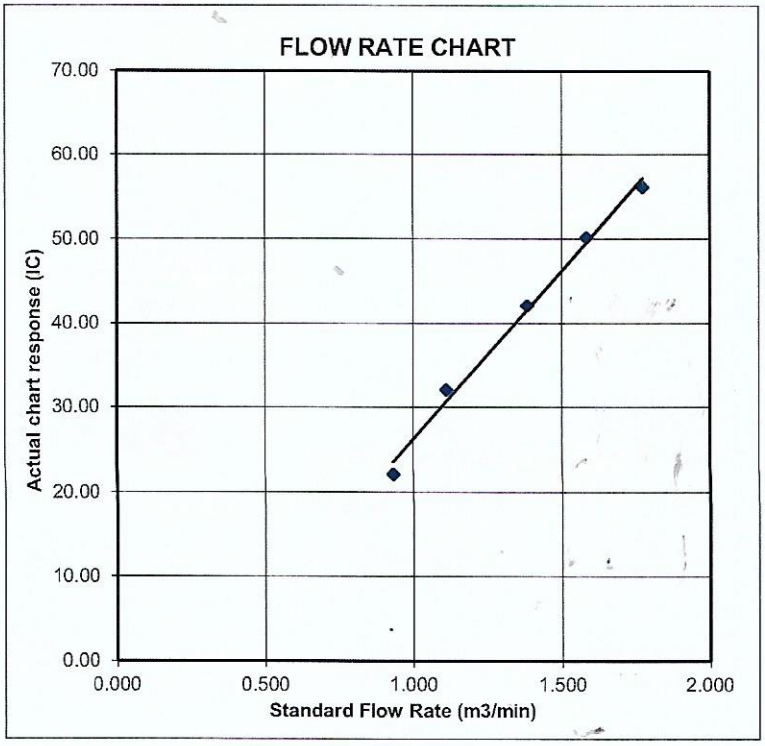

TISCH Environmental

RECALIBRATION DUE DATE:
January 19, 2022

Certificate of Calibration

Calibration Certification Information				
Cal. Date:	January 19, 2021	**Rootsmeter S/N:** 438320	**Ta:** 294	°K
Operator:	Jim Tisch		**Pa:** 755.1	mm Hg
Calibration Model #:	TE-5025A	**Calibrator S/N:** **1941**		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0420	6.4	4.00
3	5	6	1	0.9290	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7340	12.9	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H\left(Ta/Pa\right)}$ (y-axis)
1.0029	0.6762	1.4192	0.9958	0.6715	0.8824
0.9986	0.9583	2.0071	0.9915	0.9516	1.2479
0.9965	1.0726	2.2440	0.9894	1.0650	1.3952
0.9954	1.1260	2.3535	0.9883	1.1180	1.4633
0.9899	1.3487	2.8385	0.9829	1.3391	1.7648
QSTD	**m=**	**2.10574**	**QA**	**m=**	**1.31858**
	b=	**-0.00985**		**b=**	**-0.00612**
	r=	**0.99992**		**r=**	**0.99992**

Calculations

Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	**Va=**	ΔVol((Pa-ΔP)/Pa)
Qstd=	Vstd/ΔTime	**Qa=**	Va/ΔTime

For subsequent flow rate calculations:

Qstd= $1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$

Qa= $1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg

Key
ΔH: calibrator manometer reading (in H2O)
ΔP: rootsmeter manometer reading (mm Hg)
Ta: actual absolute temperature (°K)
Pa: actual barometric pressure (mm Hg)
b: intercept
m: slope

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
145 South Miami Avenue
Village of Cleves, OH 45002

www.tisch-env.com
TOLL FREE: (877)263-7610
FAX: (513)467-9009

ENVIROTECH SERVICES CO.

High-Volume TSP Sampler
5-Point Calibration Record

Location : ASR1
Calibrated by : P.F.Yeung
Date : 24/02/2022

Sampler
Model : TE-5170
Serial Number : S/N0816

Calibration Orifice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 27 December 2021
Slope (m) : 2.07035
Intercept (b) : -0.003737
Correlation Coefficient(r) : 0.99990

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1024
Ta(K) : 286

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC (indicated flow)	Y
1	18 holes	11.6	3.495	1.706	52	53.367
2	13 holes	9.2	3.113	1.522	46	47.209
3	10 holes	6.6	2.637	1.292	41	42.078
4	7 holes	4.4	2.153	1.058	33	33.868
5	5 holes	2.4	1.590	0.786	25	25.657

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b ,Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):29.862 Intercept(b): 2.432 Correlation Coefficient(r): 0.9983

Checked by: Magnum Fan Date: 26/02/2022

ENVIROTECH SERVICES CO.

High-Volume TSP Sampler
5-Point Calibration Record

Location : ARS2A
Calibrated by : P.F.Yeung
Date : 24/02/2022

Sampler
Model : TE-5170
Serial Number : S/N0890

Calibration Orifice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 27 December 2021
Slope (m) : 2.07035
Intercept (b) : -0.003737
Correlation Coefficient(r) : 0.99990

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1024
Ta(K) : 286

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	11.4	3.465	1.692	57	58.50
2	13 holes	9.1	3.096	1.513	51	52.34
3	10 holes	7.1	2.735	1.339	43	44.13
4	7 holes	4.4	2.153	1.058	34	34.89
5	5 holes	2.6	1.655	0.817	24	24.63

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b, Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):38.568 Intercept(b):-6.617 Correlation Coefficient(r): 0.9988

Checked by: Magnum Fan Date: 26/02/2022

ENVIROTECH SERVICES CO.

High-Volume TSP Sampler
5-Point Calibration Record

Location : ASR3
Calibrated by : P.F.Yeung
Date : 24/02/2022

Sampler
Model : TE-5170
Serial Number : S/N0764

Calibration Orifice and Standard Calibration Relationship
Serial Number : 2454
Service Date : 27 December 2021
Slope (m) : 2.07035
Intercept (b) : -0.003737
Correlation Coefficient(r) : 0.99990

Standard Condition
Pstd (hpa) : 1013
Tstd (K) : 298.18

Calibration Condition
Pa (hpa) : 1024
Ta(K) : 286

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1	18 holes	12.0	3.555	1.735	60	61.6
2	13 holes	9.8	3.213	1.570	53	54.4
3	10 holes	7.2	2.754	1.348	47	48.2
4	7 holes	4.8	2.248	1.104	40	41.1
5	5 holes	2.8	1.717	0.848	32	32.8

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b, Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):31.467 Intercept(b):6.053 Correlation Coefficient(r): 0.9976

Checked by: Magnum Fan Date: 26/02/2022

ENVIROTECH SERVICES CO.

High-Volume TSP Sampler
5-Point Calibration Record

Location	:	ASR4
Calibrated by	:	P.F.Yeung
Date	:	24/02/2022

Sampler

Model	:	TE-5170
Serial Number	:	S/N1068

Calibration Orfice and Standard Calibration Relationship

Serial Number	:	2454
Service Date	:	27 December 2021
Slope (m)	:	2.07035
Intercept (b)	:	-0.003737
Correlation Coefficient(r)	:	0.99990

Standard Condition

Pstd (hpa)	:	1013
Tstd (K)	:	298.18

Calibration Condition

Pa (hpa)	:	1024
Ta(K)	:	286

Resistance Plate		dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC (indicated flow)	Y
1	18 holes	12.6	3.643	1.778	52	53.37
2	13 holes	9.2	3.113	1.522	46	47.21
3	10 holes	7.2	2.754	1.348	40	41.05
4	7 holes	4.6	2.201	1.081	33	33.87
5	5 holes	2.9	1.748	0.862	25	25.66

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b ,Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):30.212 Intercept(b): 0.4065 Correlation Coefficient(r): 0.9974

Checked by: Magnum Fan Date: 26/02/2022

TISCH Environmental

RECALIBRATION DUE DATE:
December 27, 2022

Certificate of Calibration

Calibration Certification Information					
Cal. Date:	December 27, 2021	**Rootsmeter S/N:** 438320	**Ta:** 295	°K	
Operator:	Jim Tisch		**Pa:** 740.4	mm Hg	
Calibration Model #:	TE-5025A	**Calibrator S/N:** **2454**			

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4130	3.2	2.00
2	3	4	1	0.9970	6.4	4.00
3	5	6	1	0.8950	7.9	5.00
4	7	8	1	0.8480	8.8	5.50
5	9	10	1	0.7060	12.7	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H\left(Ta/Pa\right)}$ (y-axis)
0.9799	0.6935	1.4029	0.9957	0.7047	0.8927
0.9756	0.9786	1.9841	0.9914	0.9943	1.2624
0.9736	1.0879	2.2183	0.9893	1.1054	1.4114
0.9724	1.1467	2.3265	0.9881	1.1652	1.4803
0.9673	1.3700	2.8059	0.9828	1.3921	1.7853
QSTD	**m=**	**2.07035**	**QA**	**m=**	**1.29642**
	b=	**-0.03737**		**b=**	**-0.02378**
	r=	**0.99990**		**r=**	**0.99990**

Calculations

Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	**Va=**	ΔVol((Pa-ΔP)/Pa)
Qstd=	Vstd/ΔTime	**Qa=**	Va/ΔTime

For subsequent flow rate calculations:

Qstd= $1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$

Qa= $1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg

Key
ΔH: calibrator manometer reading (in H2O)
ΔP: rootsmeter manometer reading (mm Hg)
Ta: actual absolute temperature (°K)
Pa: actual barometric pressure (mm Hg)
b: intercept
m: slope

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc.
145 South Miami Avenue
Village of Cleves, OH 45002

www.tisch-env.com
TOLL FREE: (877)263-7610
FAX: (513)467-9009

Appendix E

Calibration Record

(Noise Monitoring)

輝創工程有限公司
Sun Creation Engineering Limited
Calibration & Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C212881
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-0837) Date of Receipt / 收件日期 : 30 April 2021

Description / 儀器名稱	:	Sound Level Meter
Manufacturer / 製造商	:	Rion
Model No. / 型號	:	NL-52
Serial No. / 編號	:	00542913
Supplied By / 委託者	:	Envirotech Services Co. Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun, New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (50 ± 25)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 17 May 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試 : Cheuk
K P Cheuk
Project Engineer

Certified By 核證 :
K C Lee
Engineer

Date of Issue 簽發日期 : 18 May 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 - 校正及檢測實驗所
c/o 香港新界屯門興安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Certificate of Calibration
校正證書

Certificate No. : C212881
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C210084
CL281	Multifunction Acoustic Calibrator	AV210017

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L_A	A	Fast	94.00	1	93.9	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L_A	A	Fast	94.00	1	93.9 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L_A	A	Fast	94.00	1	93.9	Ref.
			Slow			93.9	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里 1號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Certificate of Calibration
校正證書

Certificate No. : C212881
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L_A	A	Fast	94.00	63 Hz	67.6	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.5
					250 Hz	85.2	-8.6 ± 1.4
					500 Hz	90.7	-3.2 ± 1.4
					1 kHz	93.9	Ref.
					2 kHz	95.1	+1.2 ± 1.6
					4 kHz	94.9	+1.0 ± 1.6
					8 kHz	92.9	-1.1 (+2.1 ; -3.1)
					16 kHz	85.9	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L_C	C	Fast	94.00	63 Hz	93.0	-0.8 ± 1.5
					125 Hz	93.7	-0.2 ± 1.5
					250 Hz	93.9	0.0 ± 1.4
					500 Hz	93.9	0.0 ± 1.4
					1 kHz	93.9	Ref.
					2 kHz	93.7	-0.2 ± 1.6
					4 kHz	93.1	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1 ; -3.1)
					16 kHz	84.0	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 - 校正及檢測實驗所
c/o 香港新界屯門興安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

輝創工程有限公司
Sun Creation Engineering Limited
Calibration & Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C212881
證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 13748

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :
Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 - 校正及檢測實驗所
c/o 香港新界屯門興安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

輝創工程有限公司
Sun Creation Engineering Limited
Calibration & Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C214063
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-1260) Date of Receipt / 收件日期 : 28 June 2021

Description / 儀器名稱	:	Precision Acoustic Calibrator
Manufacturer / 製造商	:	LARSON DAVIS
Model No. / 型號	:	CAL200
Serial No. / 編號	:	16878
Supplied By / 委託者	:	Envirotech Services Co. Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun, New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (50 ± 25)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 13 July 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試 : Cheuk
K P Cheuk
Project Engineer

Certified By 核證 :
K C Lee
Engineer

Date of Issue 簽發日期 : 15 July 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里 一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

輝創工程有限公司
Sun Creation Engineering Limited
Calibration & Testing Laboratory

Certificate of Calibration
校正證書

Certificate No. : C214063
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C213954
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C201309

4. Test procedure : MA100N.

5. Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.9	± 0.2	± 0.2
114 dB, 1 kHz	113.9		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :
Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory
c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
輝創工程有限公司 – 校正及檢測實驗所
c/o 香港新界屯門興安里一號四樓
Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Appendix E

Calibration Record

(Water Quality Monitoring)

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BA120147
Date of Issue : 30 December 2021

PART A - CUSTOMER INFORMATION

Enovative Environmental Service Ltd.
Flat 2207, Yu Fun House Yu Chui Court, Shatin
New Territories (HK) Hong Kong
Attn :

PART B - SAMPLE INFORMATION

Name of Equipment :	YSI ProDSS (Multi-Parameters)
Manufacturer :	YSI (a xylem brand)
Serial Number :	17E100747
Date of Received :	24 December 2021
Date of Calibration :	24 December 2021
Date of Next Calibration :	23 March 2022

PART C - REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Test Parameter	Reference Method
Turbidity	APHA 21e 2130B
Conductivity	APHA 21e 2510B
Dissolved oxygen	APHA 21e 4500 O
pH value	APHA 21e 4500 H+
Salinity	APHA 21e 2520B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure

PART D - CALIBRATION RESULT

(1) Turbidity

EXPECTED READING (NTU)	DISPLAY READING (NTU)	TOLERANCE (%)	RESULT
0	0.10	--	Satisfactory
10	9.88	-1.2	Satisfactory
20	19.79	-1.1	Satisfactory
100	100.26	0.3	Satisfactory
800	808.37	1.0	Satisfactory

Tolerance of Turbidity should be less than ± 10.0 (%)

(2) Conductivity

EXPECTED READING (MS/CM AT 25°C)	DISPLAY READING (MS/CM AT 25°C)	TOLERANCE (%)	RESULT
146.9	151.2	2.92	Satisfactory
1412	1348	-4.53	Satisfactory
12890	12591	-2.32	Satisfactory
58670	57734	-1.60	Satisfactory
111900	111592	-0.28	Satisfactory

Tolerance of Conductivity should be less than ± 10.0 (%)

--- CONTINUED ON NEXT PAGE ---

AUTHORIZED SIGNATORY:

LEE Chun-ning
Assistant Manager (Chemical Testing)

This report shall not be reproduced unless with prior written approval from this laboratory

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BA120147
Date of Issue : 30 December 2021

(3) Dissolved oxygen

EXPECTED READING (MG/L)	DISPLAY READING (MG/L)	TOLERANCE (MG/L)	RESULT
7.65	7.76	0.11	Satisfactory
6.09	6.17	0.08	Satisfactory
3.20	3.28	0.08	Satisfactory
0.78	0.56	-0.22	Satisfactory

Tolerance of Dissolved oxygen should be less than ± 0.5 (mg/L)

(4) pH value

TARGET (PH UNIT)	DISPLAY READING (PH UNIT)	TOLERANCE	RESULT
4.00	4.04	0.04	Satisfactory
7.42	7.46	0.04	Satisfactory
10.01	10.13	0.12	Satisfactory

Tolerance of pH value should be less than ± 0.2 (pH unit)

(5) Salinity

EXPECTED READING (G/L)	DISPLAY READING (G/L)	TOLERANCE (%)	RESULT
10	9.93	-0.70	Satisfactory
20	19.89	-0.55	Satisfactory
30	30.20	0.67	Satisfactory

Tolerance of Salinity should be less than ± 0.0 (%)

(6) Temperature

READING OF REF. THERMOMETER (°C)	DISPLAY READING (°C)	TOLERANCE (°C)	RESULT
10	9.9	-0.1	Satisfactory
20	20.0	0.0	Satisfactory
40	40.0	0.0	Satisfactory

Tolerance of Temperature should be less than ± 2.0 (°C)

Remark(s)

·The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.
·The results relate only to the calibrated equipment as received
·The performance of the equipment stated is checked with independent reference material and results compared against a calibrated secondary source.
·"Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.
·The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

--- END OF REPORT ---

This report shall not be reproduced unless with prior written approval from this laboratory

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BB030068
Date of Issue : 21 March 2022
Page No. : 1 of 2

PART A - CUSTOMER INFORMATION

Enovative Environmental Service Ltd.
Flat 2207, Yu Fun House Yu Chui Court, Shatin
New Territories (HK) Hong Kong
Attn :

PART B - SAMPLE INFORMATION

Name of Equipment :	YSI ProDSS (Multi-Parameters)
Manufacturer :	YSI (a xylem brand)
Serial Number :	S/N: 16H104233
Date of Received :	18 March 2022
Date of Calibration :	18 March 2022
Date of Next Calibration :	17 June 2022

PART C - REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Test Parameter	Reference Method
Turbidity	APHA 21e 2130B
Conductivity	APHA 21e 2510B
Dissolved oxygen	APHA 21e 4500 O
pH value	APHA 21e 4500 H+
Salinity	APHA 21e 2520B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure

PART D - CALIBRATION RESULT

(1) Turbidity

EXPECTED READING (NTU)	DISPLAY READING (NTU)	TOLERANCE (%)	RESULT
0	0.05	--	Satisfactory
10	10.09	0.9	Satisfactory
20	19.68	-1.6	Satisfactory
100	104.79	4.79	Satisfactory
800	793.41	-0.82	Satisfactory

Tolerance of Turbidity should be less than ± 10.0 (%)

(2) Conductivity

EXPECTED READING (MS/CM AT 25°C)	DISPLAY READING	TOLERANCE (%)	RESULT
146.9	149.71	1.91	Satisfactory
1412	1471	4.18	Satisfactory
12890	12690	-1.55	Satisfactory
58670	57736	-1.59	Satisfactory
111900	110653	-1.11	Satisfactory

Tolerance of Conductivity should be less than ± 10.0 (%)

(3) Dissolved oxygen

--- CONTINUED ON NEXT PAGE ---

AUTHORIZED SIGNATORY:

LEE Chun-ning
Assistant Manager (Chemical Testing)

This report shall not be reproduced unless with prior written approval from this laboratory

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BB030068
Date of Issue : 21 March 2022

EXPECTED READING (MG/L)	DISPLAY READING (MG/L)	TOLERANCE (MG/L)	RESULT
8.08	8.23	0.15	Satisfactory
4.8	4.92	0.12	Satisfactory
1.8	1.81	0.01	Satisfactory
0.08	0.33	0.25	Satisfactory

Tolerance of Dissolved oxygen should be less than ± 0.5 (mg/L)

(4) pH value

TARGET (PH UNIT)	DISPLAY READING (PH UNIT)	TOLERANCE	RESULT
4.00	4.09	0.09	Satisfactory
7.42	7.49	0.07	Satisfactory
10.01	9.87	-0.14	Satisfactory

Tolerance of pH value should be less than ± 0.2 (pH unit)

(5) Salinity

EXPECTED READING (G/L)	DISPLAY READING (G/L)	TOLERANCE (%)	RESULT
10	9.9	-1.00	Satisfactory
20	19.83	-0.85	Satisfactory
30	30.33	1.10	Satisfactory

Tolerance of Salinity should be less than ± 10.0 (%)

(6) Temperature

READING OF REF. THERMOMETER (°C)	DISPLAY READING (°C)	TOLERANCE (°C)	RESULT
10	10	0	Satisfactory
20	20	0	Satisfactory
48	48	0	Satisfactory

Tolerance of Temperature should be less than ± 2.0 (°C)

Remark(s)

·The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.

·The results relate only to the calibrated equipment as received

·The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

·"Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.

·The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

--- END OF REPORT ---

This report shall not be reproduced unless with prior written approval from this laboratory

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BB030069
Date of Issue : 21 March 2022
Page No. : 1 of 2

PART A - CUSTOMER INFORMATION

Enovative Environmental Service Ltd.
Flat 2207, Yu Fun House Yu Chui Court, Shatin
New Territories (HK) Hong Kong
Attn :

PART B - SAMPLE INFORMATION

Name of Equipment :	YSI ProDSS (Multi-Parameters)
Manufacturer :	YSI (a xylem brand)
Serial Number :	S/N: 16H104234
Date of Received :	18 March 2022
Date of Calibration :	18 March 2022
Date of Next Calibration :	17 June 2022

PART C - REFERENCE METHODS/ DOCUMENTS FOR THE CALIBRATION

Test Parameter	Reference Method
Turbidity	APHA 21e 2130B
Conductivity	APHA 21e 2510B
Dissolved oxygen	APHA 21e 4500 O
pH value	APHA 21e 4500 H+
Salinity	APHA 21e 2520B
Temperature	Section 6 of international Accreditation New Zealand Technical Guide no. 3 Second edition March 2008: Working Thermometer Calibration Procedure

PART D - CALIBRATION RESULT

(1) Turbidity

EXPECTED READING (NTU)	DISPLAY READING (NTU)	TOLERANCE (%)	RESULT
0	0.05	--	Satisfactory
10	10.20	2.0	Satisfactory
20	19.77	-1.2	Satisfactory
100	104.21	4.2	Satisfactory
800	792.60	-0.9	Satisfactory

Tolerance of Turbidity should be less than ± 10.0 (%)

(2) Conductivity

EXPECTED READING (MS/CM AT 25°C)	DISPLAY READING	TOLERANCE (%)	RESULT
146.9	152.1	3.54	Satisfactory
1412	1472	4.25	Satisfactory
12890	12618	-2.11	Satisfactory
58670	57412	-2.14	Satisfactory
111900	110616	-1.15	Satisfactory

Tolerance of Conductivity should be less than ± 10.0 (%)

(3) Dissolved oxygen

--- CONTINUED ON NEXT PAGE ---

AUTHORIZED SIGNATORY:

LEE Chun-ning
Assistant Manager (Chemical Testing)

This report shall not be reproduced unless with prior written approval from this laboratory

專業化驗有限公司
QUALITY PRO TEST-CONSULT LIMITED
Unit 10, 14/F, Wah Wai Centre, 38-40 Au Pui Wan St., Fotan, Hong Kong
Email: info@qualityprotest.com; Website: www.qualityprotest.com
Tel: (852) 3956 8717; Fax: (852) 3956 3928

REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION

Test Report No. : R-BB030069
Date of Issue : 21 March 2022

EXPECTED READING (MG/L)	DISPLAY READING (MG/L)	TOLERANCE (MG/L)	RESULT
8.08	8.25	0.17	Satisfactory
4.8	5.00	0.20	Satisfactory
1.8	1.74	-0.06	Satisfactory
0.08	0.5	0.42	Satisfactory

Tolerance of Dissolved oxygen should be less than ± 0.5 (mg/L)

(4) pH value

TARGET (PH UNIT)	DISPLAY READING (PH UNIT)	TOLERANCE	RESULT
4.00	4.08	0.08	Satisfactory
7.42	7.47	0.05	Satisfactory
10.01	9.90	-0.11	Satisfactory

Tolerance of pH value should be less than ± 0.2 (pH unit)

(5) Salinity

EXPECTED READING (G/L)	DISPLAY READING (G/L)	TOLERANCE (%)	RESULT
10	9.93	-0.70	Satisfactory
20	19.81	-0.95	Satisfactory
30	30.12	0.40	Satisfactory

Tolerance of Salinity should be less than ± 10.0 (%)

(6) Temperature

READING OF REF. THERMOMETER (°C)	DISPLAY READING (°C)	TOLERANCE (°C)	RESULT
10	10	0	Satisfactory
20	20	0	Satisfactory
48	48	0	Satisfactory

Tolerance of Temperature should be less than ± 2.0 (°C)

Remark(s)

·The "Date of Next Calibration" is recommended according to best practice principals as practiced by QPT or quoted form relevant international standards.

·The results relate only to the calibrated equipment as received

·The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

·"Displayed Reading" denotes the figure shown on item under calibration/ checking regardless of equipment precision or significant figures.

·The "Tolerance Limit" mentioned is the acceptance criteria applicable for similar equipment used by Quality Pro Test-Consult Ltd. or quoted form relevant international standards.

--- END OF REPORT ---

This report shall not be reproduced unless with prior written approval from this laboratory

F. Graphical Plots of the Monitoring Results

Air Quality

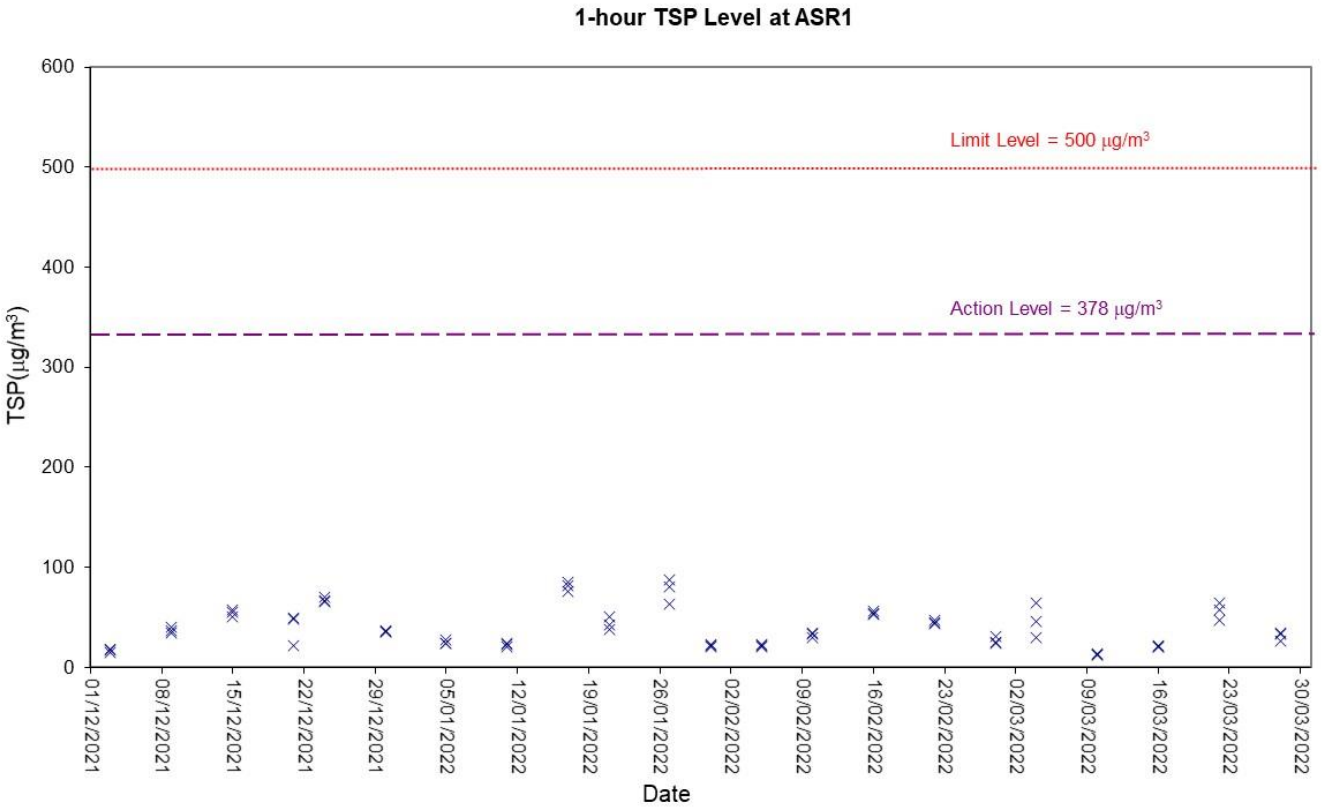
1-hour TSP Level at ASR1
Limit Level = 500 μg/m³
Action Level = 378 μg/m³
TSP(μg/m³)
Date
600
500
400
300
200
100
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

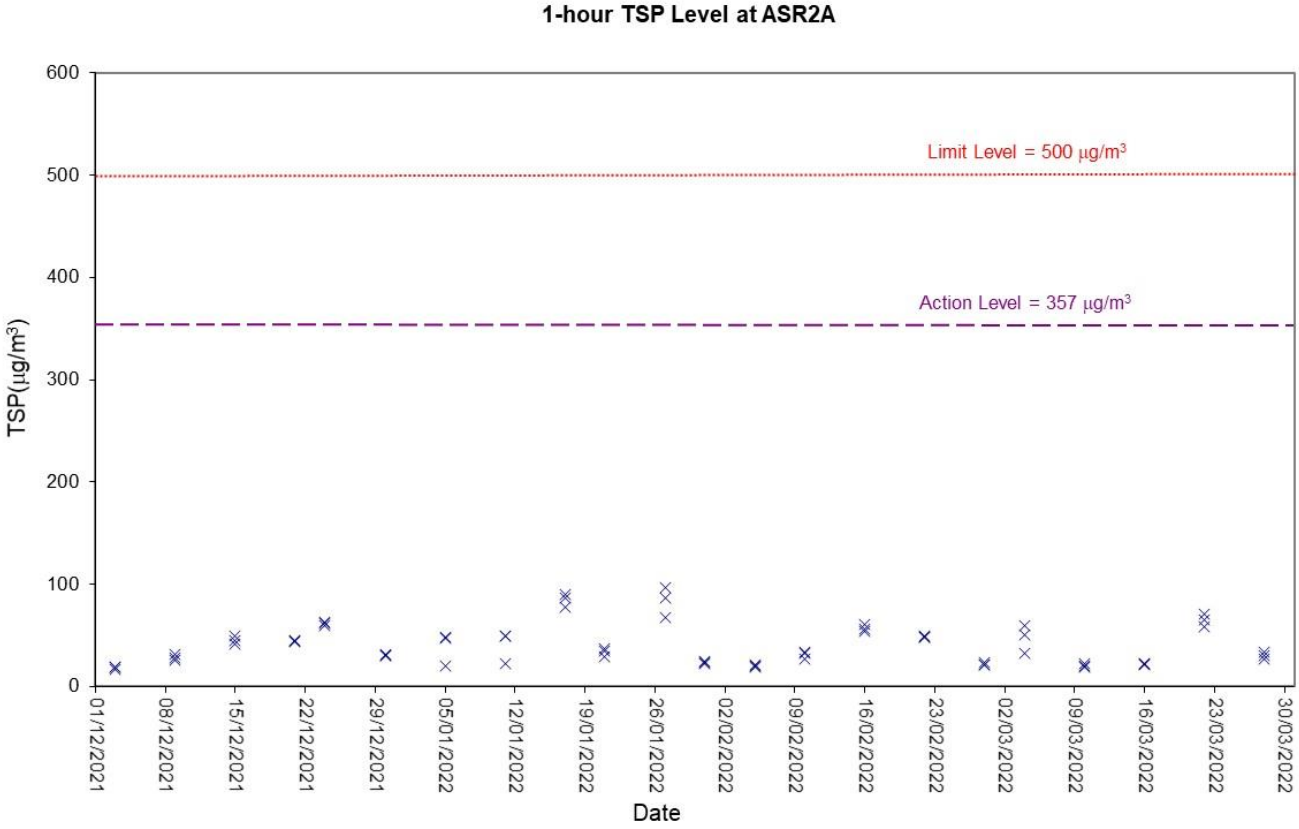
1-hour TSP Level at ASR2A
Limit Level = 500 μg/m³
Action Level = 357 μg/m³
TSP(μg/m³)
Date
600
500
400
300
200
100
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

Air Quality

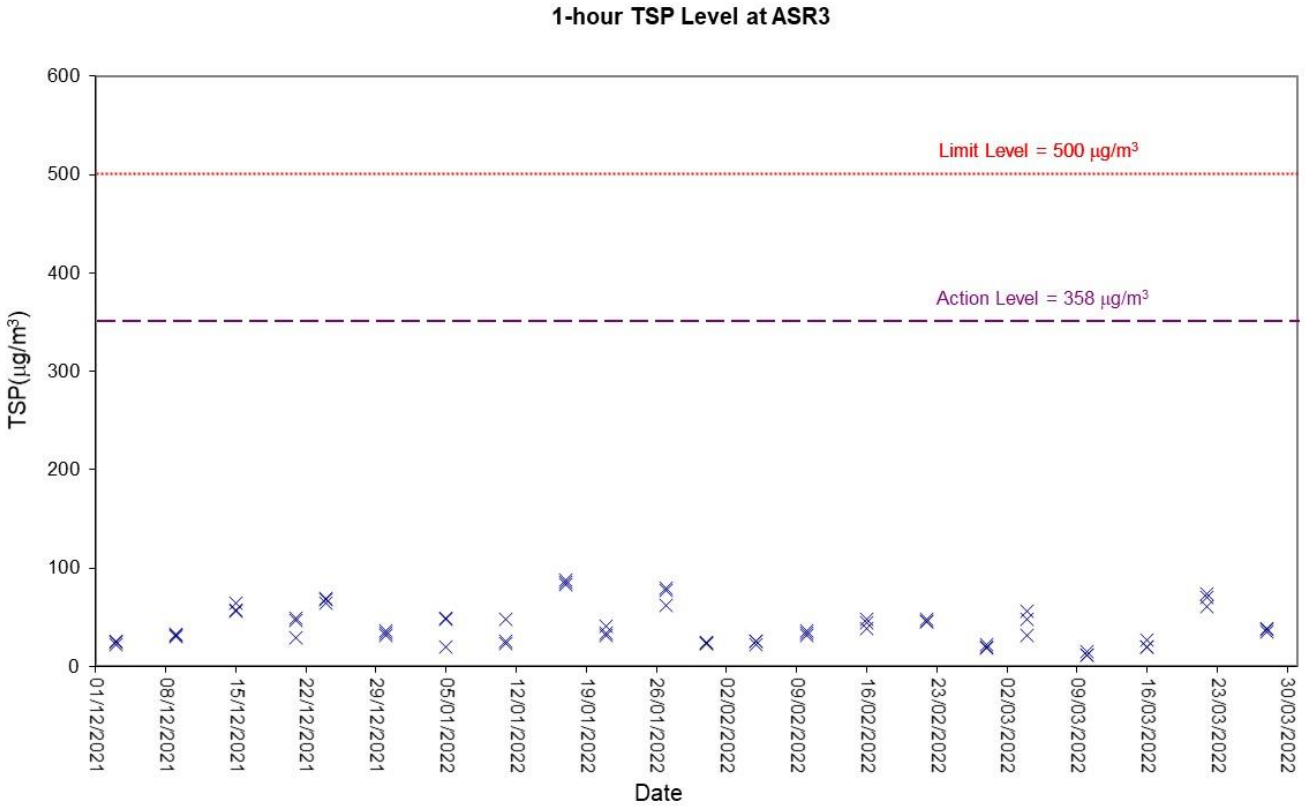
1-hour TSP Level at ASR3
600
500
400
300
200
100
0
TSP(µg/m³)
Limit Level = 500 µg/m³
Action Level = 358 µg/m³
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

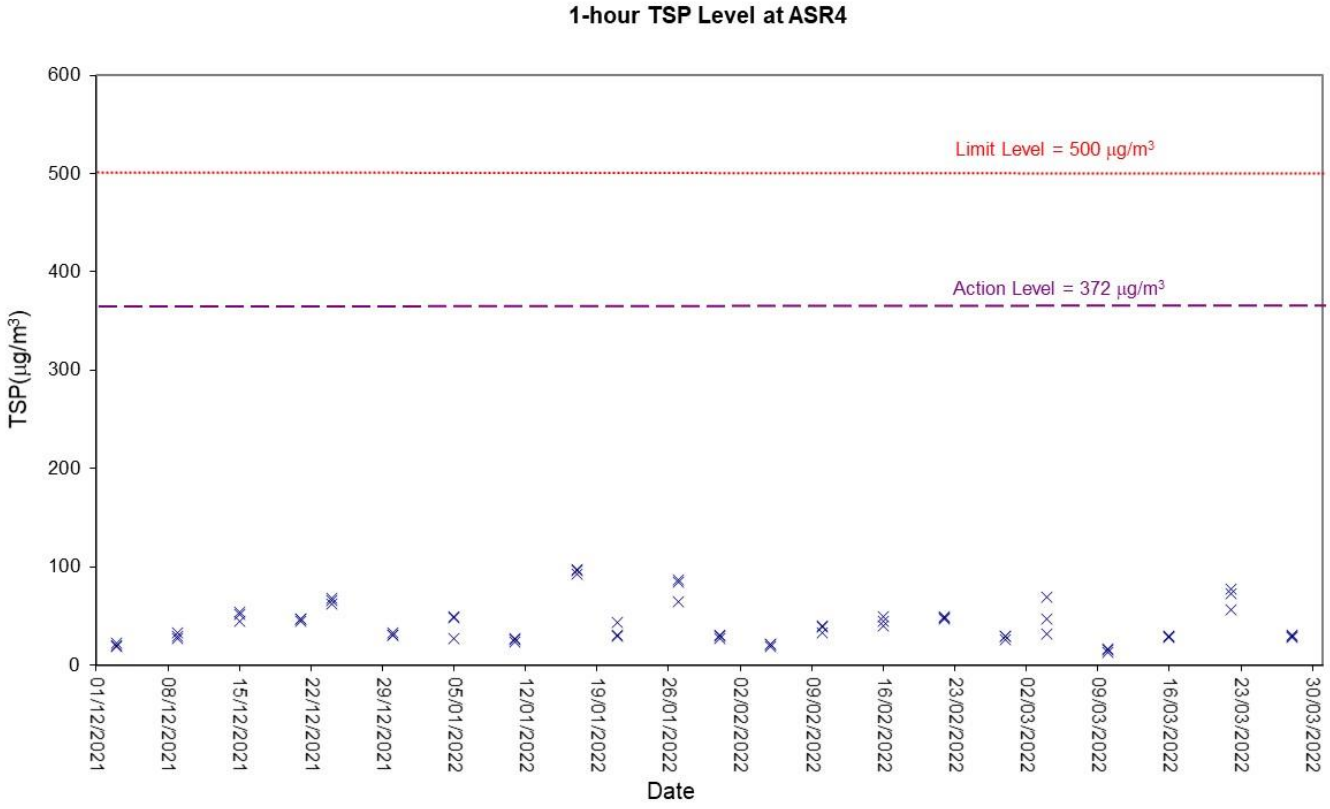
1-hour TSP Level at ASR4
600
500
400
300
200
100
0
TSP(µg/m³)
Limit Level = 500 µg/m³
Action Level = 372 µg/m³
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

Air Quality

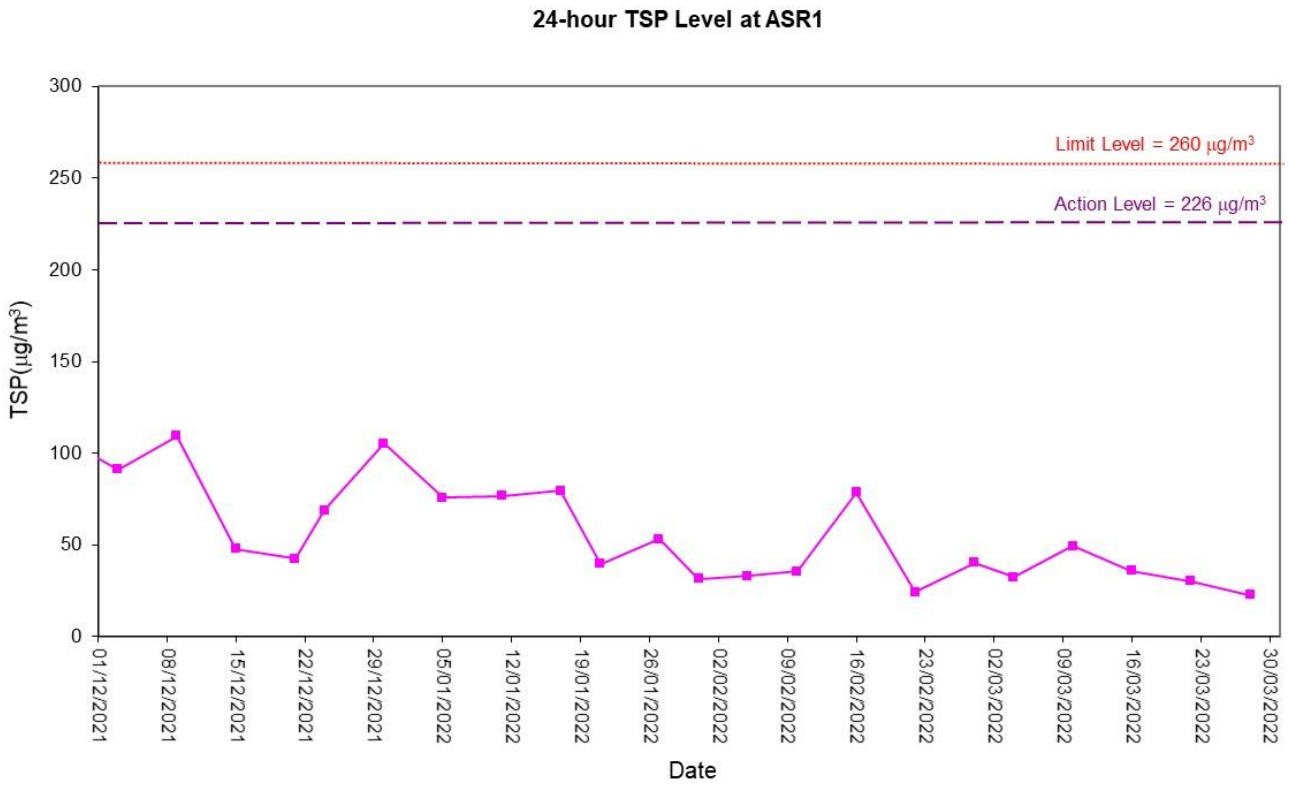
24-hour TSP Level at ASR1
Limit Level = 260 μg/m³
Action Level = 226 μg/m³
TSP(μg/m³)
300
250
200
150
100
50
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

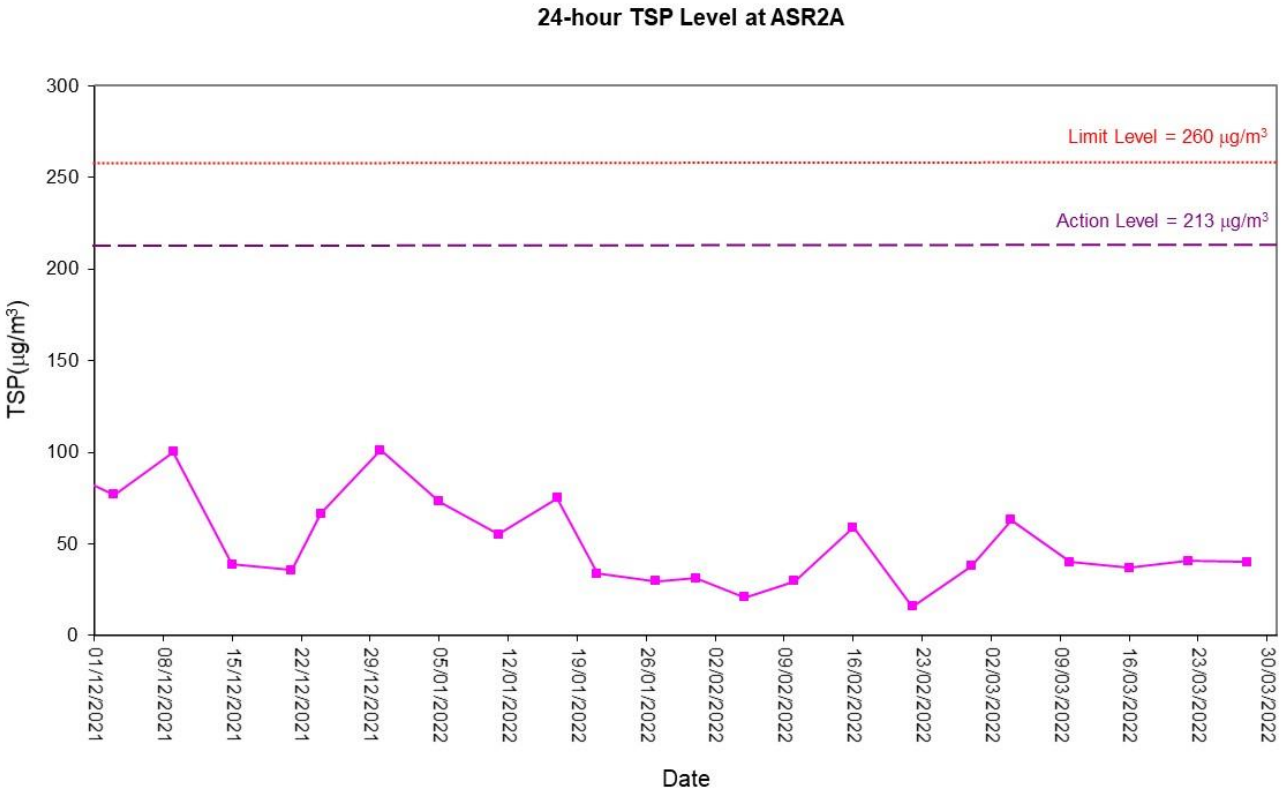
24-hour TSP Level at ASR2A
Limit Level = 260 μg/m³
Action Level = 213 μg/m³
TSP(μg/m³)
300
250
200
150
100
50
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

Air Quality

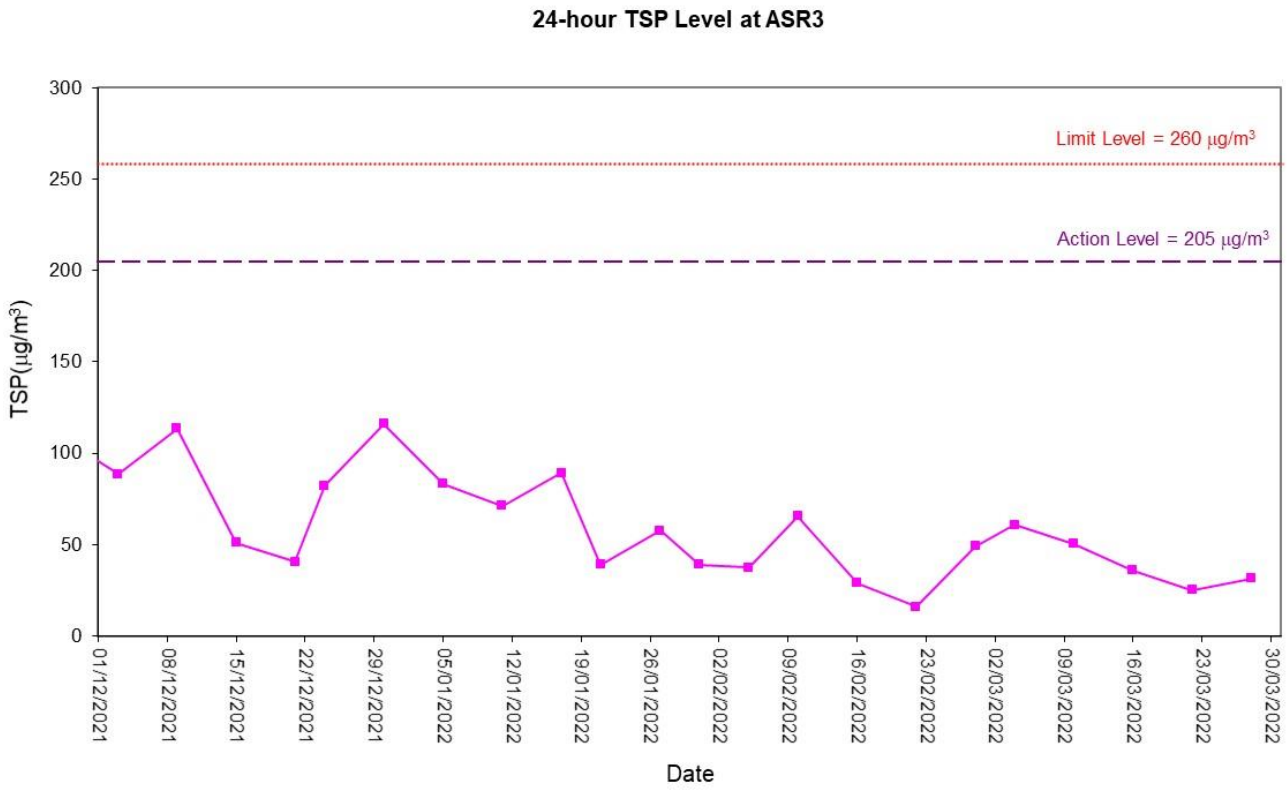
24-hour TSP Level at ASR3
Limit Level = 260 μg/m³
Action Level = 205 μg/m³
TSP(μg/m³)
300
250
200
150
100
50
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

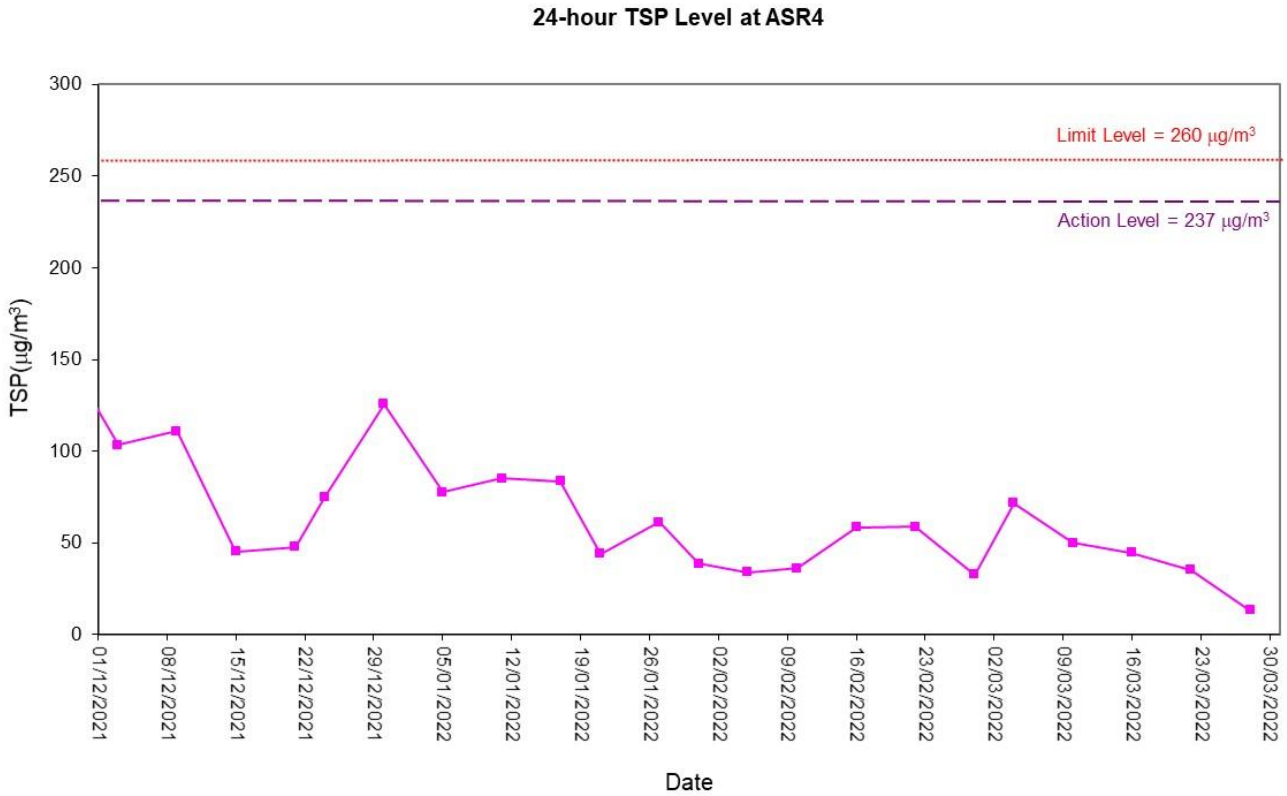
24-hour TSP Level at ASR4
Limit Level = 260 μg/m³
Action Level = 237 μg/m³
TSP(μg/m³)
300
250
200
150
100
50
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022
Date

Noise

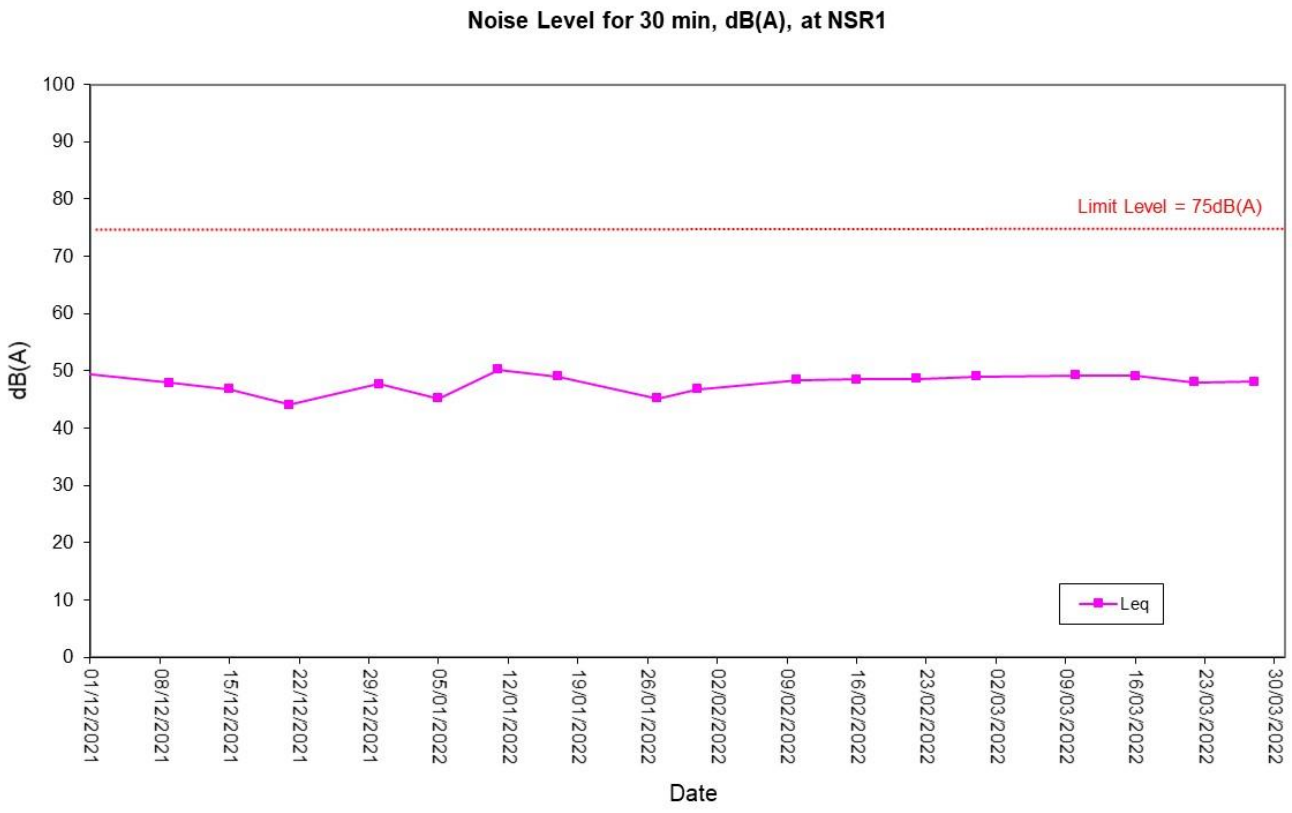
Noise Level for 30 min, dB(A), at NSR1
dB(A)
Limit Level = 75dB(A)
Leq
Date
100
90
80
70
60
50
40
30
20
10
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

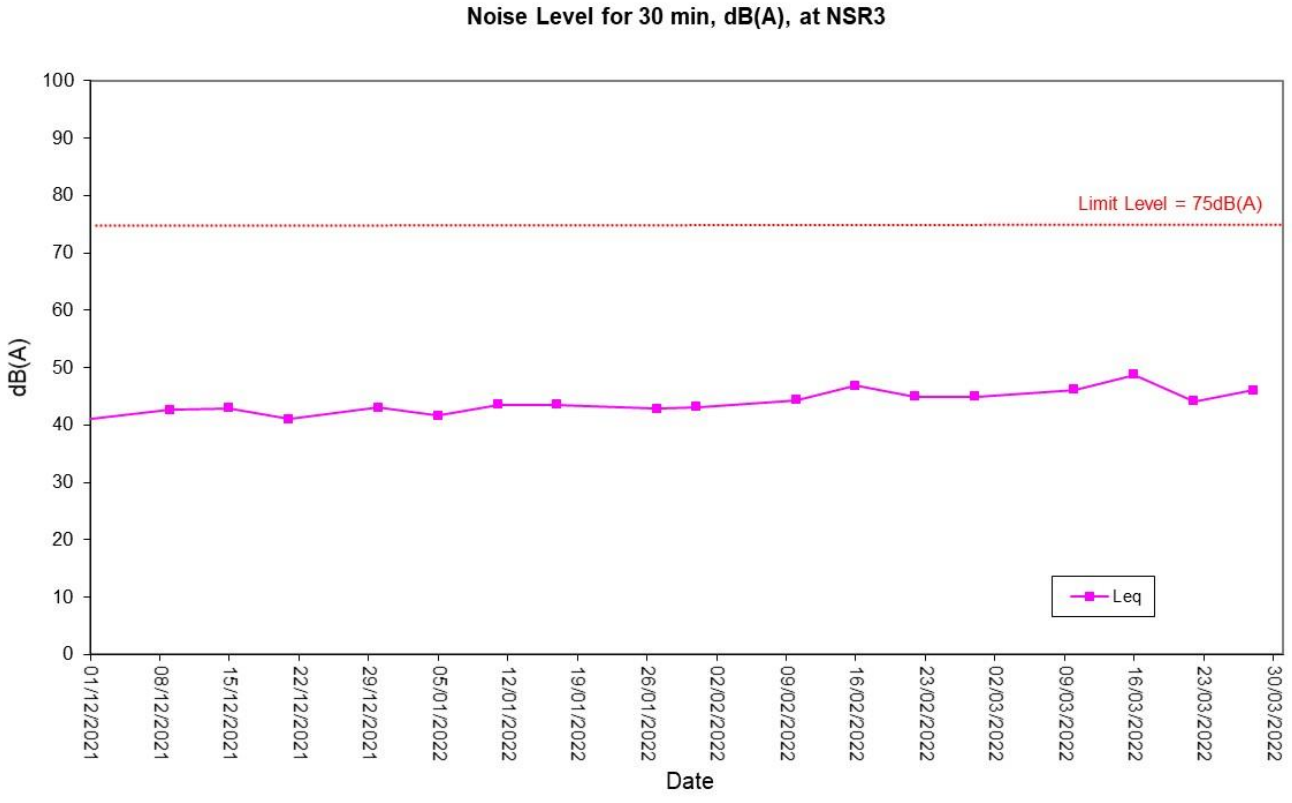
Noise Level for 30 min, dB(A), at NSR3
dB(A)
Limit Level = 75dB(A)
Leq
Date
100
90
80
70
60
50
40
30
20
10
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

Noise

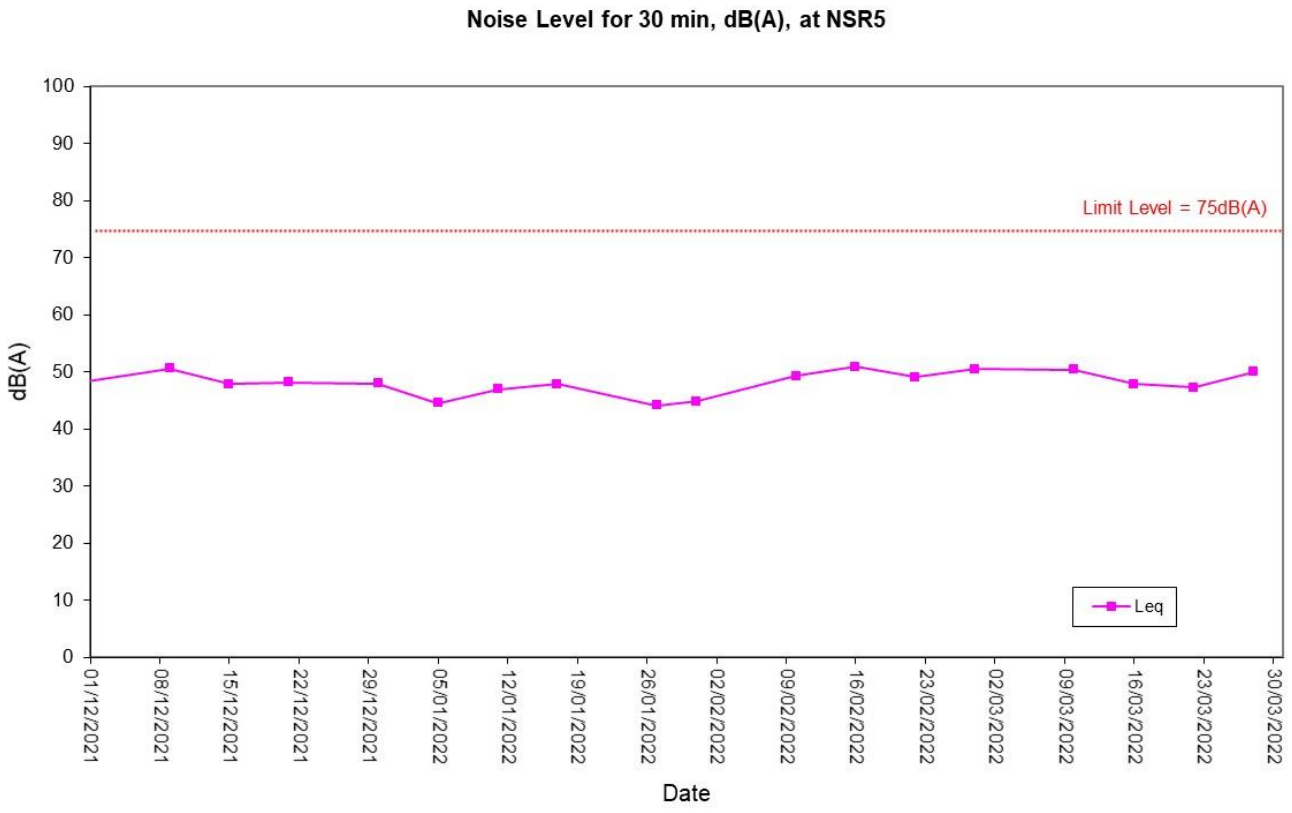
Noise Level for 30 min, dB(A), at NSR5
dB(A)
Limit Level = 75dB(A)
Leq
Date
100
90
80
70
60
50
40
30
20
10
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

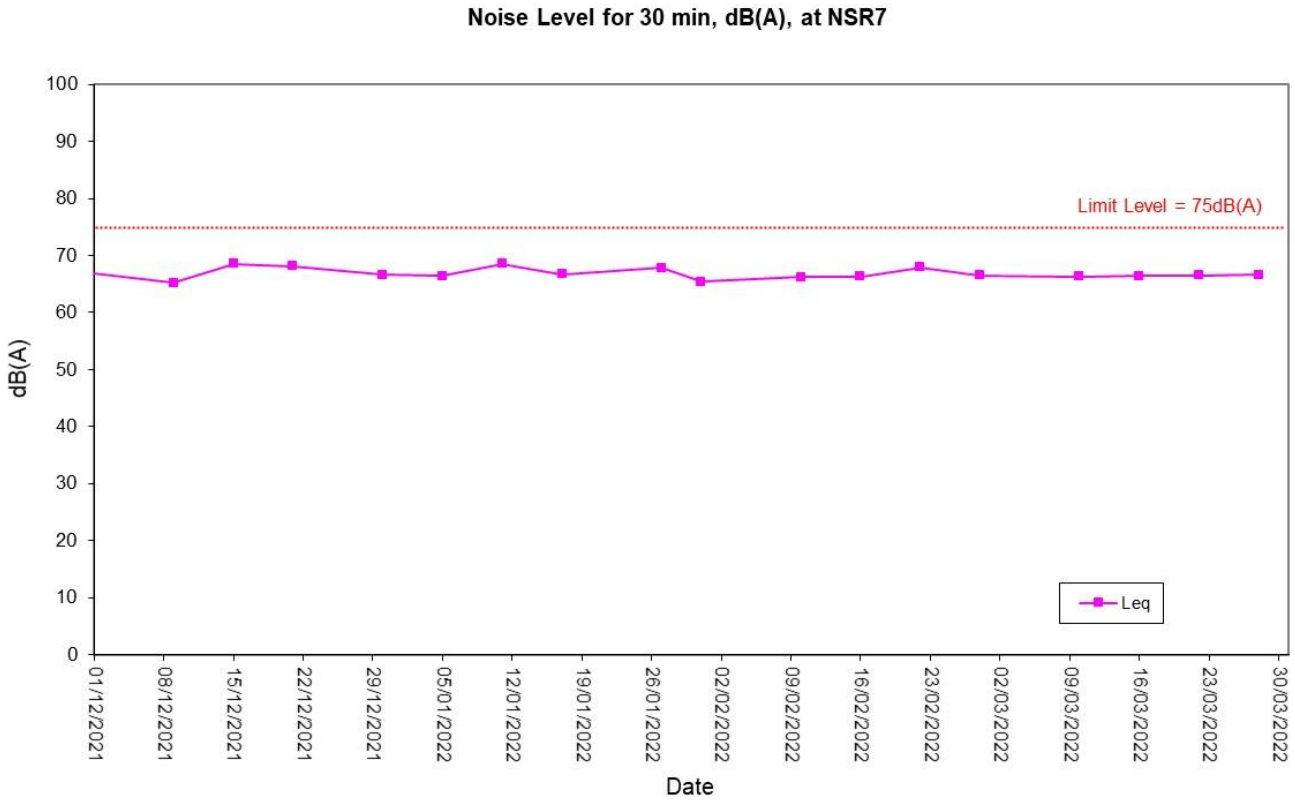
Noise Level for 30 min, dB(A), at NSR7
dB(A)
Limit Level = 75dB(A)
Leq
Date
100
90
80
70
60
50
40
30
20
10
0
01/12/2021
08/12/2021
15/12/2021
22/12/2021
29/12/2021
05/01/2022
12/01/2022
19/01/2022
26/01/2022
02/02/2022
09/02/2022
16/02/2022
23/02/2022
02/03/2022
09/03/2022
16/03/2022
23/03/2022
30/03/2022

Water Quality

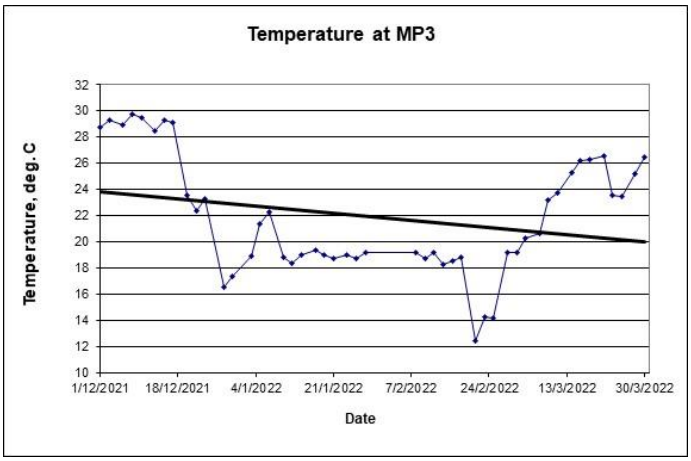

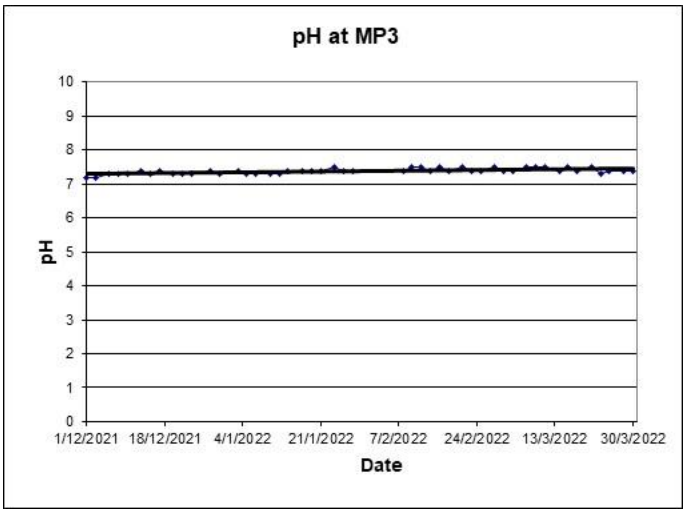

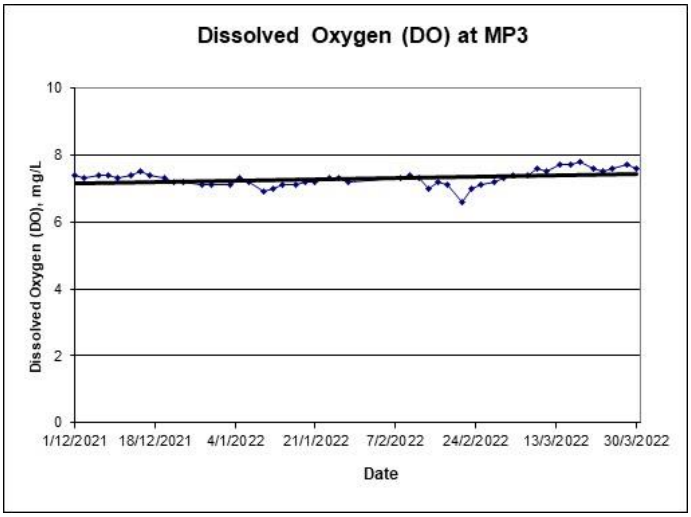

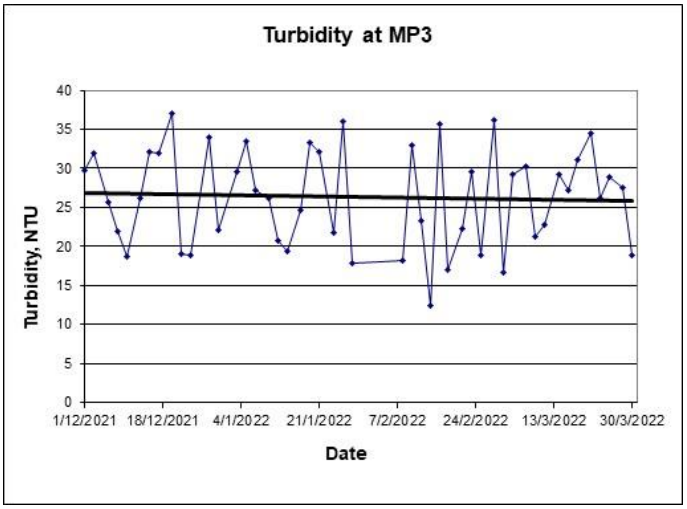

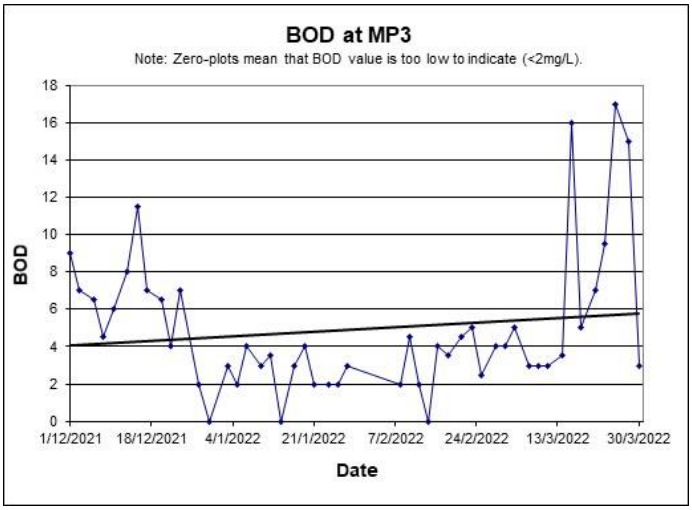

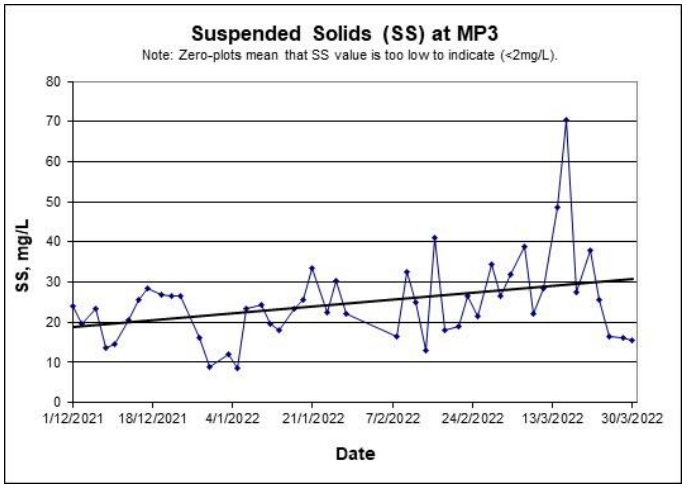

Water Quality

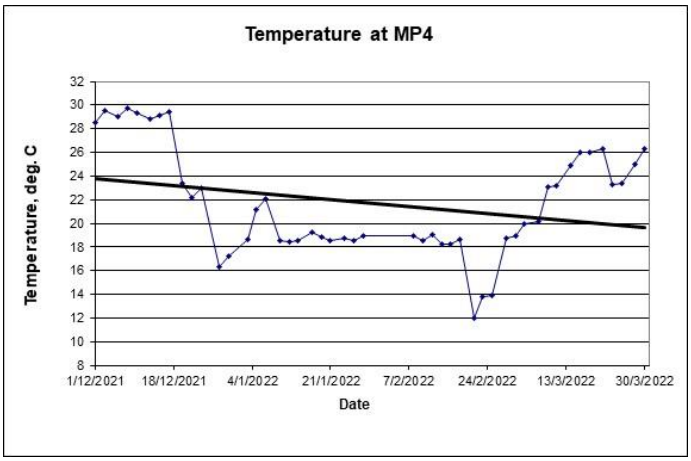

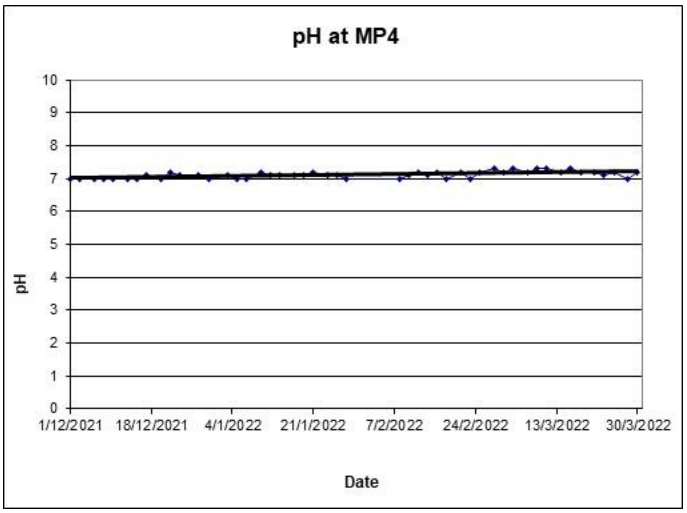

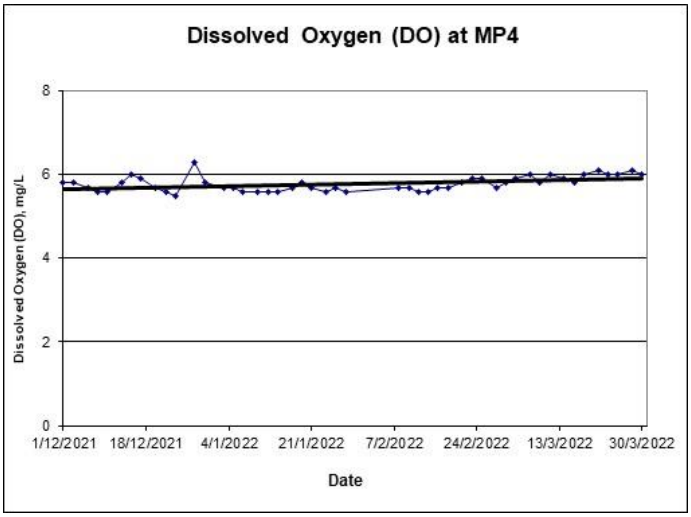

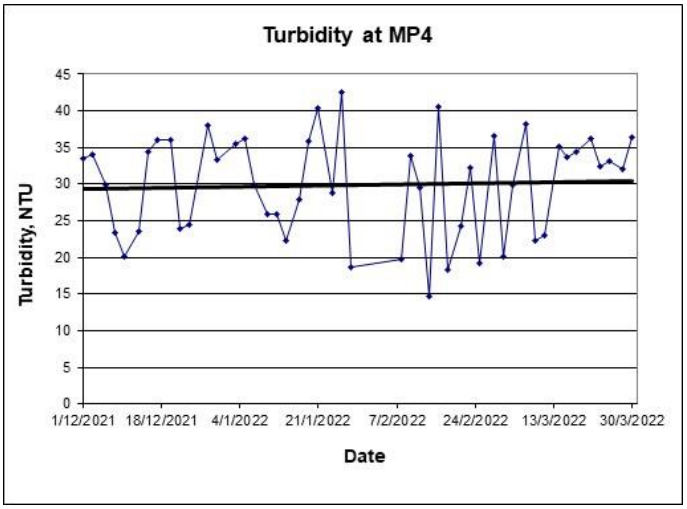

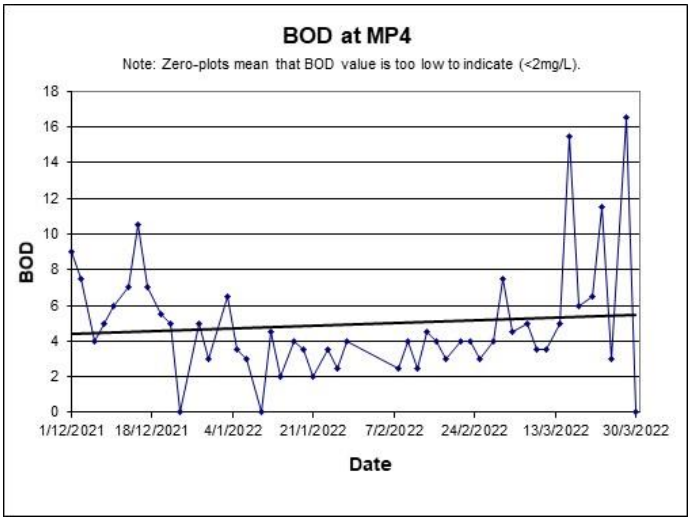

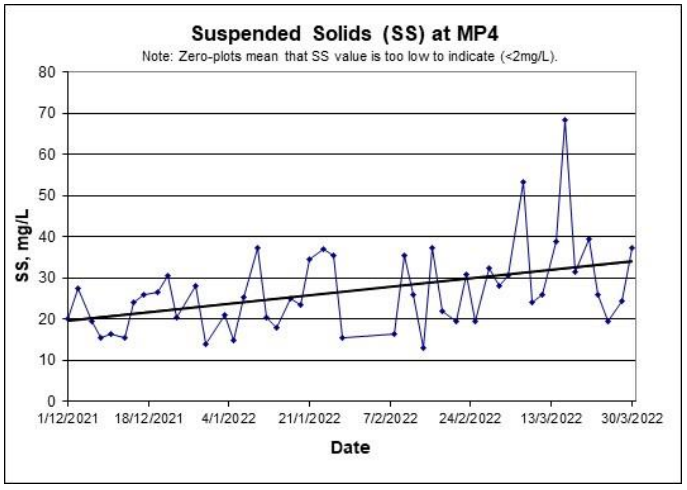

Water Quality

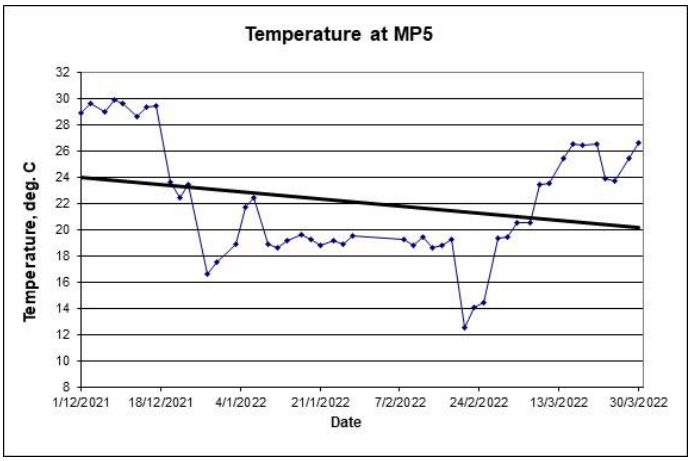

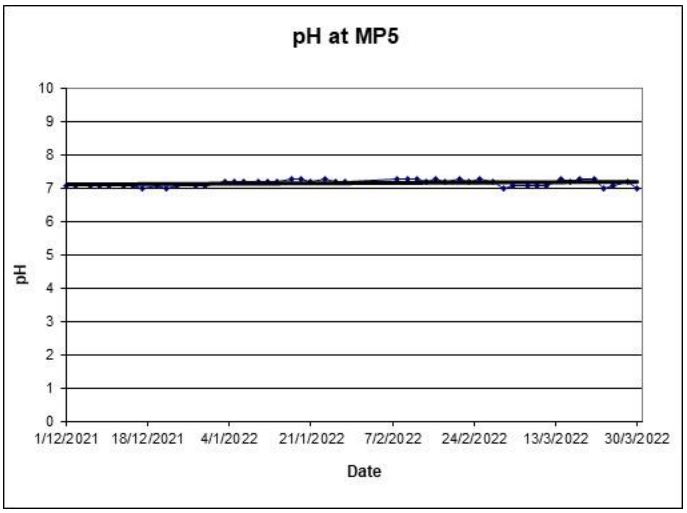

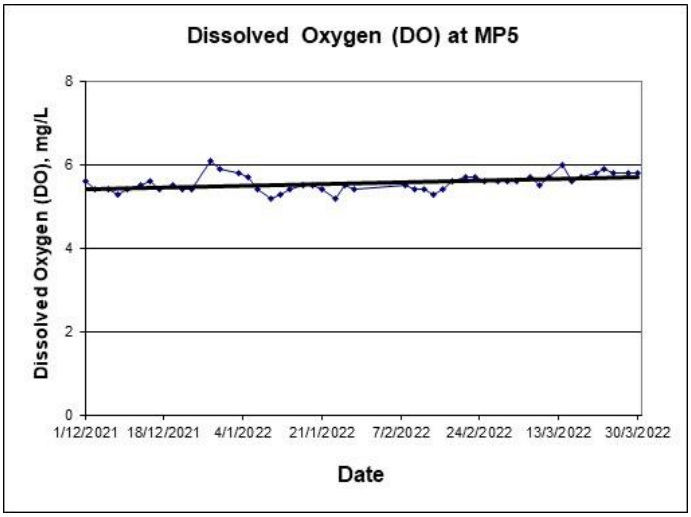

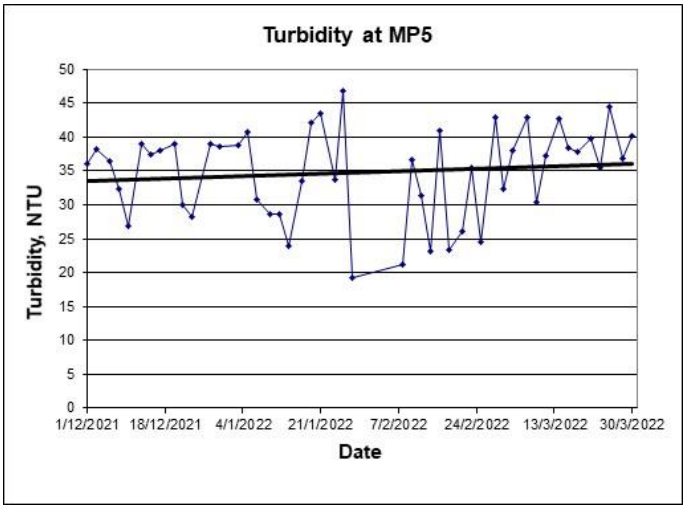

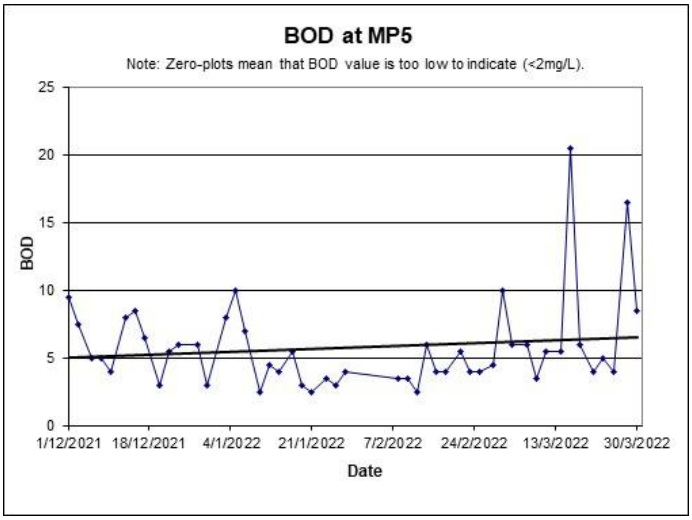

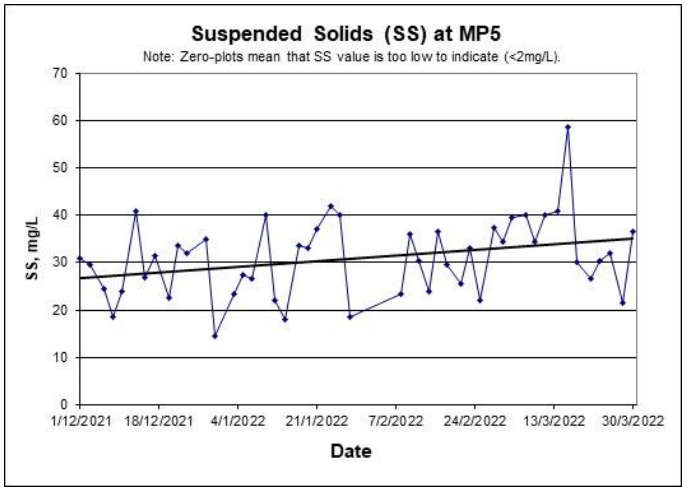

Water Quality

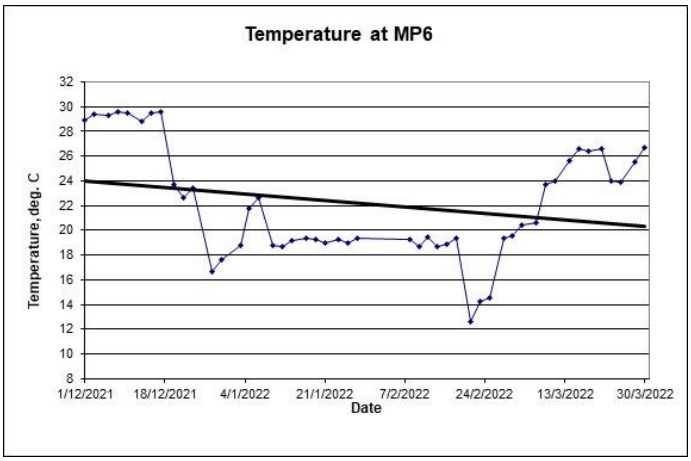

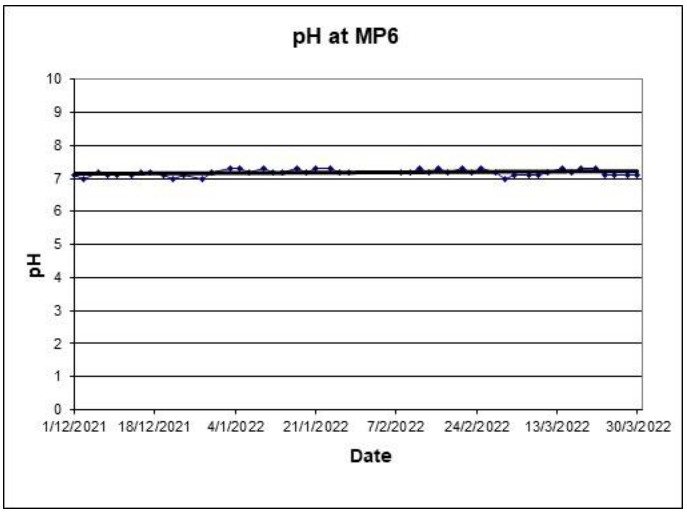

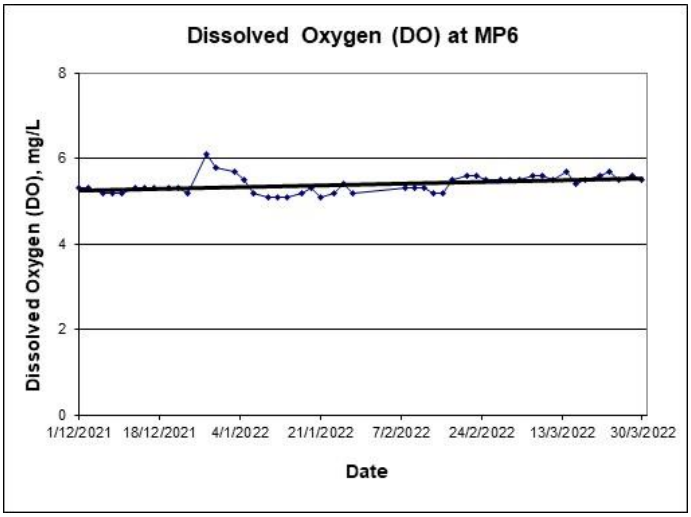

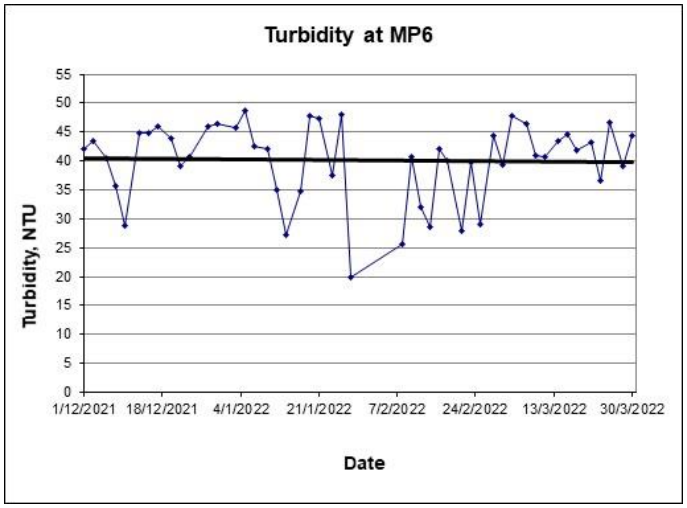

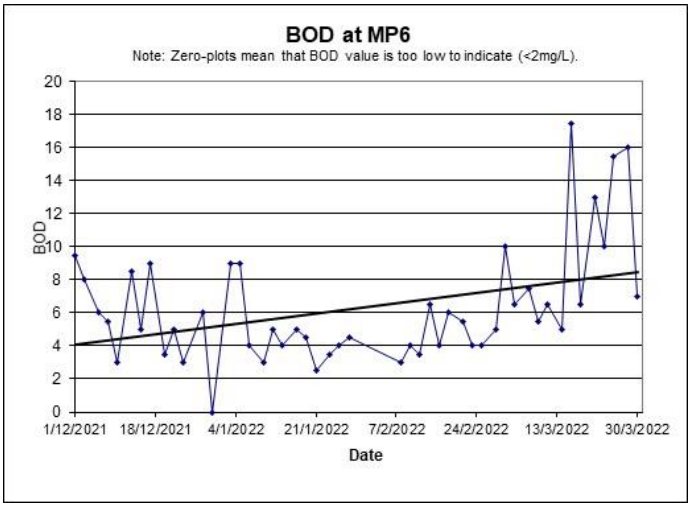

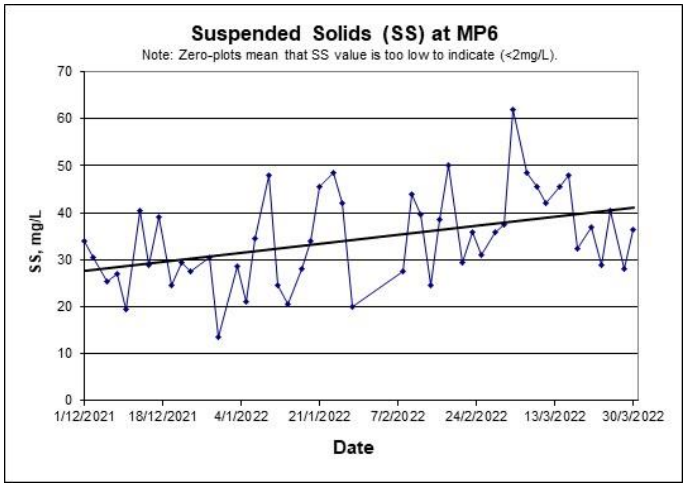

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208009
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 02-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 15-Mar-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 02-Mar-2022 to 15-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208009 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER			Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	02-Mar-2022	HK2208009-001		26	4	----	----	----
MP3-2	02-Mar-2022	HK2208009-002		27	4	----	----	----
MP4-1	02-Mar-2022	HK2208009-003		28	8	----	----	----
MP4-2	02-Mar-2022	HK2208009-004		28	7	----	----	----
MP5-1	02-Mar-2022	HK2208009-005		34	10	----	----	----
MP5-2	02-Mar-2022	HK2208009-006		35	10	----	----	----
MP6-1	02-Mar-2022	HK2208009-007		37	10	----	----	----
MP6-2	02-Mar-2022	HK2208009-008		38	10	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4225215)								
HK2207692-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	55	53	4.1
HK2208007-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	7160	7120	0.6
EA/ED: Physical and Aggregate Properties (QC Lot: 4225216)								
HK2208075-003	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	33	37	11.9
HK2208100-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	132	134	1.7

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4225215)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	100	----	76.9	120	----	----
EA/ED: Physical and Aggregate Properties (QCLot: 4225216)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	108	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4207043)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	102	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208140**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 04-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 17-Mar-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 04-Mar-2022 to 17-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208140 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER			Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	04-Mar-2022	HK2208140-001		34	5	----	----	----
MP3-2	04-Mar-2022	HK2208140-002		30	5	----	----	----
MP4-1	04-Mar-2022	HK2208140-003		30	5	----	----	----
MP4-2	04-Mar-2022	HK2208140-004		31	4	----	----	----
MP5-1	04-Mar-2022	HK2208140-005		40	6	----	----	----
MP5-2	04-Mar-2022	HK2208140-006		39	6	----	----	----
MP6-1	04-Mar-2022	HK2208140-007		58	7	----	----	----
MP6-2	04-Mar-2022	HK2208140-008		66	6	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4232617)								
HK2208141-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	44	44	0.0
HK2208141-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	45	44	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4232617)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	90.0	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4210539)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	102	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208146
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 07-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 20-Mar-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 07-Mar-2022 to 20-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208146 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER			Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	07-Mar-2022	HK2208146-001		40	3	----	----	----
MP3-2	07-Mar-2022	HK2208146-002		38	3	----	----	----
MP4-1	07-Mar-2022	HK2208146-003		50	6	----	----	----
MP4-2	07-Mar-2022	HK2208146-004		57	4	----	----	----
MP5-1	07-Mar-2022	HK2208146-005		40	6	----	----	----
MP5-2	07-Mar-2022	HK2208146-006		40	6	----	----	----
MP6-1	07-Mar-2022	HK2208146-007		51	8	----	----	----
MP6-2	07-Mar-2022	HK2208146-008		46	7	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4234569)								
HK2208146-002	MP3-2	EA025: Suspended Solids (SS)	----	2	mg/L	38	36	3.8
HK2208146-007	MP6-1	EA025: Suspended Solids (SS)	----	2	mg/L	51	51	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4234569)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	99.0	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4223308)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	105	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208414**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 09-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 21-Mar-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 09-Mar-2022 to 21-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208414 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: **WATER**		*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**	**----**	**----**	**----**
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	*Sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	09-Mar-2022	HK2208414-001	**23**	**3**	**----**	**----**	**----**
MP3-2	09-Mar-2022	HK2208414-002	**21**	**3**	**----**	**----**	**----**
MP4-1	09-Mar-2022	HK2208414-003	**24**	**4**	**----**	**----**	**----**
MP4-2	09-Mar-2022	HK2208414-004	**24**	**3**	**----**	**----**	**----**
MP5-1	09-Mar-2022	HK2208414-005	**34**	**5**	**----**	**----**	**----**
MP5-2	09-Mar-2022	HK2208414-006	**35**	**2**	**----**	**----**	**----**
MP6-1	09-Mar-2022	HK2208414-007	**45**	**7**	**----**	**----**	**----**
MP6-2	09-Mar-2022	HK2208414-008	**46**	**4**	**----**	**----**	**----**

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4237308)								
HK2208346-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	<2	<2	0.0
HK2208341-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	146	144	1.6

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4237308)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	91.5	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4223311)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	105	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208416**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 11-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 25-Mar-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 11-Mar-2022 to 25-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208416 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER			Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	11-Mar-2022	HK2208416-001		28	3	----	----	----
MP3-2	11-Mar-2022	HK2208416-002		29	3	----	----	----
MP4-1	11-Mar-2022	HK2208416-003		25	4	----	----	----
MP4-2	11-Mar-2022	HK2208416-004		27	3	----	----	----
MP5-1	11-Mar-2022	HK2208416-005		39	5	----	----	----
MP5-2	11-Mar-2022	HK2208416-006		41	6	----	----	----
MP6-1	11-Mar-2022	HK2208416-007		42	7	----	----	----
MP6-2	11-Mar-2022	HK2208416-008		42	6	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4248430)								
HK2208416-001	MP3-1	EA025: Suspended Solids (SS)	----	2	mg/L	28	30	8.2
HK2208416-002	MP3-2	EA025: Suspended Solids (SS)	----	2	mg/L	29	28	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4248430)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	108	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4226415)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	99.8	----	78.6	118	----	----
EP: Aggregate Organics (QCLot: 4226416)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	104	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208761
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 14-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 25-Mar-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 14-Mar-2022 to 25-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208761 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER		Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	14-Mar-2022	HK2208761-001	50	4	----	----	----
MP3-2	14-Mar-2022	HK2208761-002	47	3	----	----	----
MP4-1	14-Mar-2022	HK2208761-003	41	4	----	----	----
MP4-2	14-Mar-2022	HK2208761-004	37	6	----	----	----
MP5-1	14-Mar-2022	HK2208761-005	38	6	----	----	----
MP5-2	14-Mar-2022	HK2208761-006	44	5	----	----	----
MP6-1	14-Mar-2022	HK2208761-007	43	5	----	----	----
MP6-2	14-Mar-2022	HK2208761-008	48	5	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4248592)								
HK2208419-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	68	70	2.7
HK2208419-011	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	33	36	9.1

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4248592)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	104	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4226416)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	104	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208762
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 16-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 30-Mar-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 16-Mar-2022 to 30-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208762 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: **WATER**			*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**	**----**	**----**	**----**
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	*Sampling date / time*	*Laboratory sample ID*		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	16-Mar-2022	HK2208762-001		**72**	**16**	**----**	**----**	**----**
MP3-2	16-Mar-2022	HK2208762-002		**69**	**16**	**----**	**----**	**----**
MP4-1	16-Mar-2022	HK2208762-003		**66**	**17**	**----**	**----**	**----**
MP4-2	16-Mar-2022	HK2208762-004		**71**	**14**	**----**	**----**	**----**
MP5-1	16-Mar-2022	HK2208762-005		**52**	**19**	**----**	**----**	**----**
MP5-2	16-Mar-2022	HK2208762-006		**65**	**22**	**----**	**----**	**----**
MP6-1	16-Mar-2022	HK2208762-007		**47**	**17**	**----**	**----**	**----**
MP6-2	16-Mar-2022	HK2208762-008		**49**	**18**	**----**	**----**	**----**

Laboratory Duplicate (DUP) Report

- **No Laboratory Duplicate (DUP) Results are required to be reported.**

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

		Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
Method: Compound	CAS Number	LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4249576)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	104	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4236700)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	87.9	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208763**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 18-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 30-Mar-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 18-Mar-2022 to 30-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208763 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER		Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	18-Mar-2022	HK2208763-001	28	4	----	----	----
MP3-2	18-Mar-2022	HK2208763-002	27	6	----	----	----
MP4-1	18-Mar-2022	HK2208763-003	32	6	----	----	----
MP4-2	18-Mar-2022	HK2208763-004	31	6	----	----	----
MP5-1	18-Mar-2022	HK2208763-005	30	6	----	----	----
MP5-2	18-Mar-2022	HK2208763-006	30	6	----	----	----
MP6-1	18-Mar-2022	HK2208763-007	31	6	----	----	----
MP6-2	18-Mar-2022	HK2208763-008	34	7	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4253746)								
HK2208793-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	56	57	0.0
HK2208793-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	53	52	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4253746)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	100	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4237829)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	91.2	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208764
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 21-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 30-Mar-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 21-Mar-2022 to 30-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208764 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: **WATER**		*Compound*	**EA025: Suspended Solids (SS)**	**EP030: Biochemical Oxygen Demand**	**----**	**----**	**----**
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	*Sampling date / time*	*Laboratory sample ID*	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	21-Mar-2022	HK2208764-001	**39**	**7**	**----**	**----**	**----**
MP3-2	21-Mar-2022	HK2208764-002	**37**	**7**	**----**	**----**	**----**
MP4-1	21-Mar-2022	HK2208764-003	**39**	**7**	**----**	**----**	**----**
MP4-2	21-Mar-2022	HK2208764-004	**40**	**6**	**----**	**----**	**----**
MP5-1	21-Mar-2022	HK2208764-005	**26**	**4**	**----**	**----**	**----**
MP5-2	21-Mar-2022	HK2208764-006	**27**	**4**	**----**	**----**	**----**
MP6-1	21-Mar-2022	HK2208764-007	**36**	**13**	**----**	**----**	**----**
MP6-2	21-Mar-2022	HK2208764-008	**38**	**13**	**----**	**----**	**----**

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4253746)								
HK2208793-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	56	57	0.0
HK2208793-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	53	52	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4253746)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	100	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4240452)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	91.1	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208766**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 23-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 31-Mar-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 23-Mar-2022 to 31-Mar-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208766 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER		Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	23-Mar-2022	HK2208766-001	26	10	----	----	----
MP3-2	23-Mar-2022	HK2208766-002	25	9	----	----	----
MP4-1	23-Mar-2022	HK2208766-003	26	11	----	----	----
MP4-2	23-Mar-2022	HK2208766-004	26	12	----	----	----
MP5-1	23-Mar-2022	HK2208766-005	31	5	----	----	----
MP5-2	23-Mar-2022	HK2208766-006	30	5	----	----	----
MP6-1	23-Mar-2022	HK2208766-007	30	9	----	----	----
MP6-2	23-Mar-2022	HK2208766-008	28	11	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4257346)								
HK2208795-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	45	45	0.0
HK2208795-002	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	44	44	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4257346)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	96.5	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4245566)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	94.2	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208767**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 25-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 01-Apr-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 25-Mar-2022 to 01-Apr-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208767 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER			Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
			LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID		EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	25-Mar-2022	HK2208767-001		17	17	----	----	----
MP3-2	25-Mar-2022	HK2208767-002		16	17	----	----	----
MP4-1	25-Mar-2022	HK2208767-003		20	3	----	----	----
MP4-2	25-Mar-2022	HK2208767-004		19	3	----	----	----
MP5-1	25-Mar-2022	HK2208767-005		32	4	----	----	----
MP5-2	25-Mar-2022	HK2208767-006		32	4	----	----	----
MP6-1	25-Mar-2022	HK2208767-007		40	15	----	----	----
MP6-2	25-Mar-2022	HK2208767-008		41	16	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4259127)								
HK2210258-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	10100	10100	0.4
HK2210261-001	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	171	168	1.7

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4259127)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	104	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4249735)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	95.8	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYICAL CHEMISTRY & TESTING SERVICES

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	*Laboratory*	:	ALS Technichem (HK) Pty Ltd	*Page*	: 1 of 4
Contact	:	MR THOMAS WONG	*Contact*	:	Richard Fung	*Work Order*	: **HK2208769**
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	*Address*	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	*E-mail*	:	richard.fung@alsglobal.com		
Telephone	:	----	*Telephone*	:	+852 2610 1044		
Facsimile	:	----	*Facsimile*	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				*Date received*	: 28-Mar-2022
Order number	:	—	*Quote number*	:	HKE/3067/2021	*Date of issue*	: 04-Apr-2022
C-O-C number	:	—				*No. of samples*	- *Received* : 8
Site	:	—					- *Analysed* : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	*Position*	*Authorised results for:*
Fung Lim Chee, Richard	**Managing Director**	**Inorganics**

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 28-Mar-2022 to 04-Apr-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208769 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER		Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	28-Mar-2022	HK2208769-001	16	15	----	----	----
MP3-2	28-Mar-2022	HK2208769-002	16	15	----	----	----
MP4-1	28-Mar-2022	HK2208769-003	25	16	----	----	----
MP4-2	28-Mar-2022	HK2208769-004	24	17	----	----	----
MP5-1	28-Mar-2022	HK2208769-005	22	17	----	----	----
MP5-2	28-Mar-2022	HK2208769-006	21	16	----	----	----
MP6-1	28-Mar-2022	HK2208769-007	28	16	----	----	----
MP6-2	28-Mar-2022	HK2208769-008	28	16	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4261614)								
HK2208769-001	MP3-1	EA025: Suspended Solids (SS)	----	2	mg/L	16	16	0.0
HK2208797-004	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	17	17	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4261614)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	95.5	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4253591)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	98.5	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

CERTIFICATE OF ANALYSIS

Client	:	ENOVATIVE ENVIRONMENTAL SERVICE LTD	Laboratory	:	ALS Technichem (HK) Pty Ltd	Page	: 1 of 4
Contact	:	MR THOMAS WONG	Contact	:	Richard Fung	Work Order	: HK2208770
Address	:	FLAT 2207, YU FUN HSE, YU CHUI COURT, SHATIN, N.T. HONG KONG	Address	:	11/F., Chung Shun Knitting Centre, 1 - 3 Wing Yip Street, Kwai Chung, N.T., Hong Kong		
E-mail	:	thomas.wong@eno.com.hk	E-mail	:	richard.fung@alsglobal.com		
Telephone	:	----	Telephone	:	+852 2610 1044		
Facsimile	:	----	Facsimile	:	+852 2610 2021		
Project	:	PROPOSED COMPREHENSIVE DEVELOPMENT AT WO SHANG WAI YUEN LONG				Date received	: 30-Mar-2022
Order number	:	—	Quote number	:	HKE/3067/2021	Date of issue	: 06-Apr-2022
C-O-C number	:	—				No. of samples	- Received : 8
Site	:	—					- Analysed : 8

This report may not be reproduced except with prior written approval from the testing laboratory.

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatory	Position	Authorised results for:
Fung Lim Chee, Richard	Managing Director	Inorganics

General Comments

This report supersedes any previous report(s) with this reference. All pages of this report have been checked and approved for release. When sampling time information is not provided by the client, sampling dates are shown without a time component. In these instances, the time component has been assumed by the laboratory for processing purposes. Testing period is from 30-Mar-2022 to 06-Apr-2022.

Key: LOR = Limit of reporting; CAS Number = CAS registry number from database maintained by Chemical Abstracts Services. The Chemical Abstracts Service is a division of the American Chemical Society.

Specific Comments for Work Order HK2208770 :

Samples(s) was/ were submitted by client. Sample(s) arrived laboratory in chilled condition. The result(s) related only to the item(s) tested.

Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.

Analytical Results

Sub-Matrix: WATER		Compound	EA025: Suspended Solids (SS)	EP030: Biochemical Oxygen Demand	----	----	----
		LOR Unit	2 mg/L	2 mg/L	----	----	----
Sample ID	Sampling date / time	Laboratory sample ID	EA/ED: Physical and Aggregate Properties	EP: Aggregate Organics	----	----	----
MP3-1	30-Mar-2022	HK2208770-001	15	3	----	----	----
MP3-2	30-Mar-2022	HK2208770-002	16	3	----	----	----
MP4-1	30-Mar-2022	HK2208770-003	38	<2	----	----	----
MP4-2	30-Mar-2022	HK2208770-004	37	<2	----	----	----
MP5-1	30-Mar-2022	HK2208770-005	36	8	----	----	----
MP5-2	30-Mar-2022	HK2208770-006	37	9	----	----	----
MP6-1	30-Mar-2022	HK2208770-007	36	7	----	----	----
MP6-2	30-Mar-2022	HK2208770-008	37	7	----	----	----

Laboratory Duplicate (DUP) Report

Matrix: **WATER**

Laboratory sample ID	Sample ID	Method: Compound	CAS Number	Laboratory Duplicate (DUP) Report				
				LOR	Unit	Original Result	Duplicate Result	RPD (%)
EA/ED: Physical and Aggregate Properties (QC Lot: 4265582)								
HK2208770-001	MP3-1	EA025: Suspended Solids (SS)	----	2	mg/L	15	14	0.0
HK2208799-003	Anonymous	EA025: Suspended Solids (SS)	----	2	mg/L	10	10	0.0

Method Blank (MB), Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report

Matrix: **WATER**

Method: Compound	CAS Number	Method Blank (MB) Report			Laboratory Control Spike (LCS) and Laboratory Control Spike Duplicate (DCS) Report						
					Spike	Spike Recovery (%)		Recovery Limits (%)		RPDs (%)	
		LOR	Unit	Result	Concentration	LCS	DCS	Low	High	Value	Control Limit
EA/ED: Physical and Aggregate Properties (QCLot: 4265582)											
EA025: Suspended Solids (SS)	----	2	mg/L	<2	10 mg/L	95.0	----	76.9	120	----	----
EP: Aggregate Organics (QCLot: 4258782)											
EP030: Biochemical Oxygen Demand	----	----	mg/L	----	198 mg/L	99.2	----	78.6	118	----	----

Matrix Spike (MS) and Matrix Spike Duplicate (MSD) Report

- **No Matrix Spike (MS) or Matrix Spike Duplicate (MSD) Results are required to be reported.**

G. Weather Conditions during the Monitoring Period

Wind Data for Wetland Park

4 March 2022

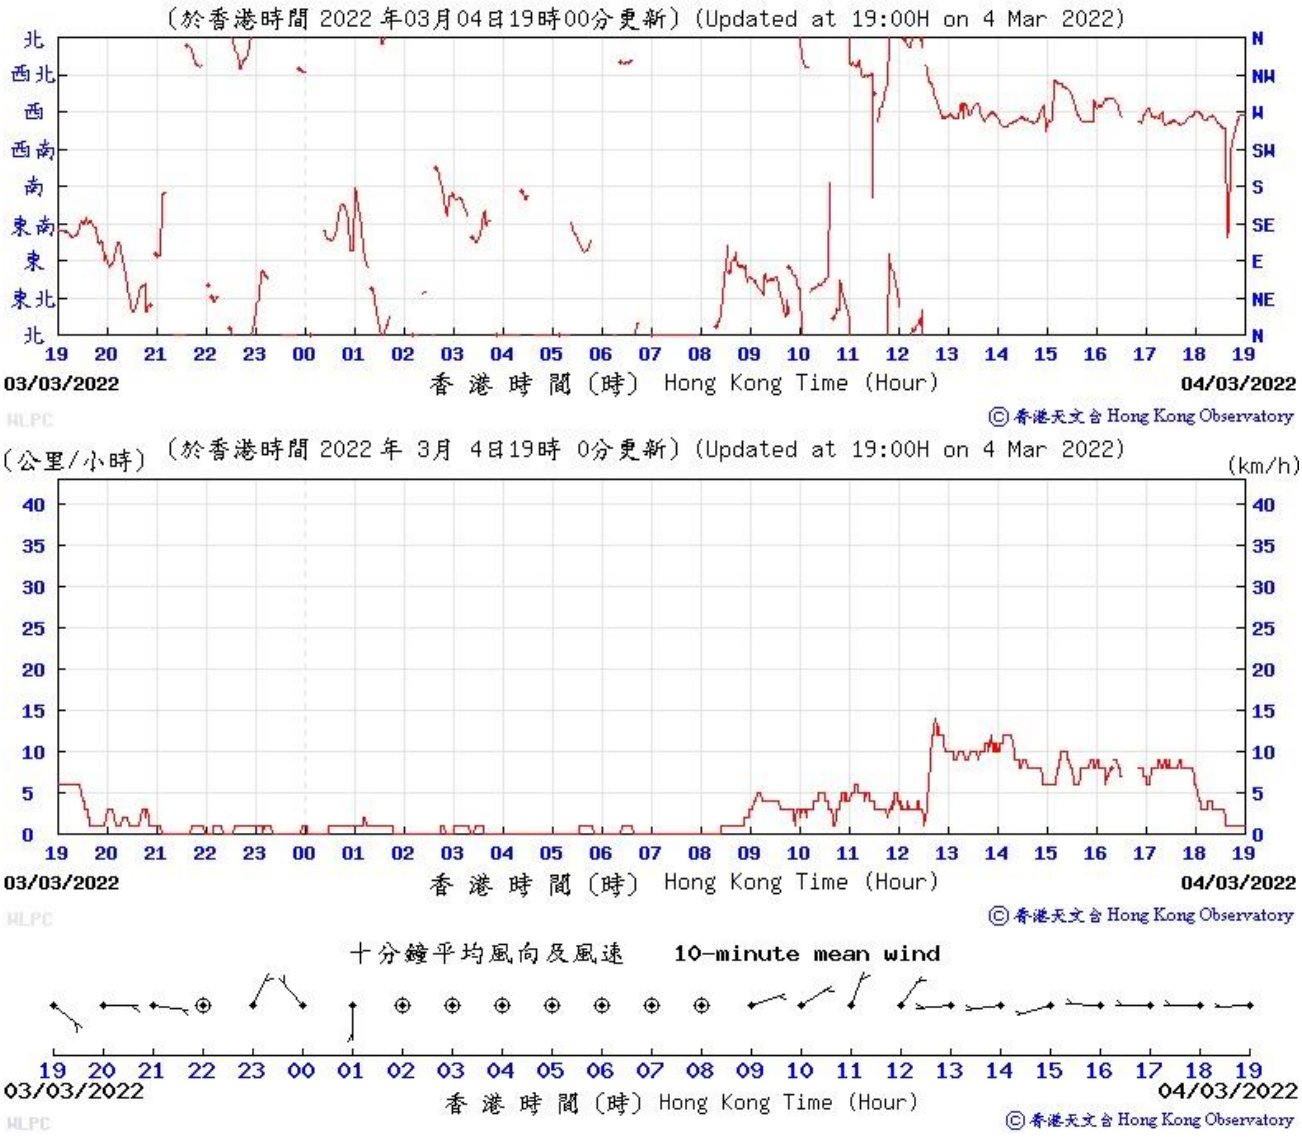

Wind Data for Wetland Park

5 March 2022

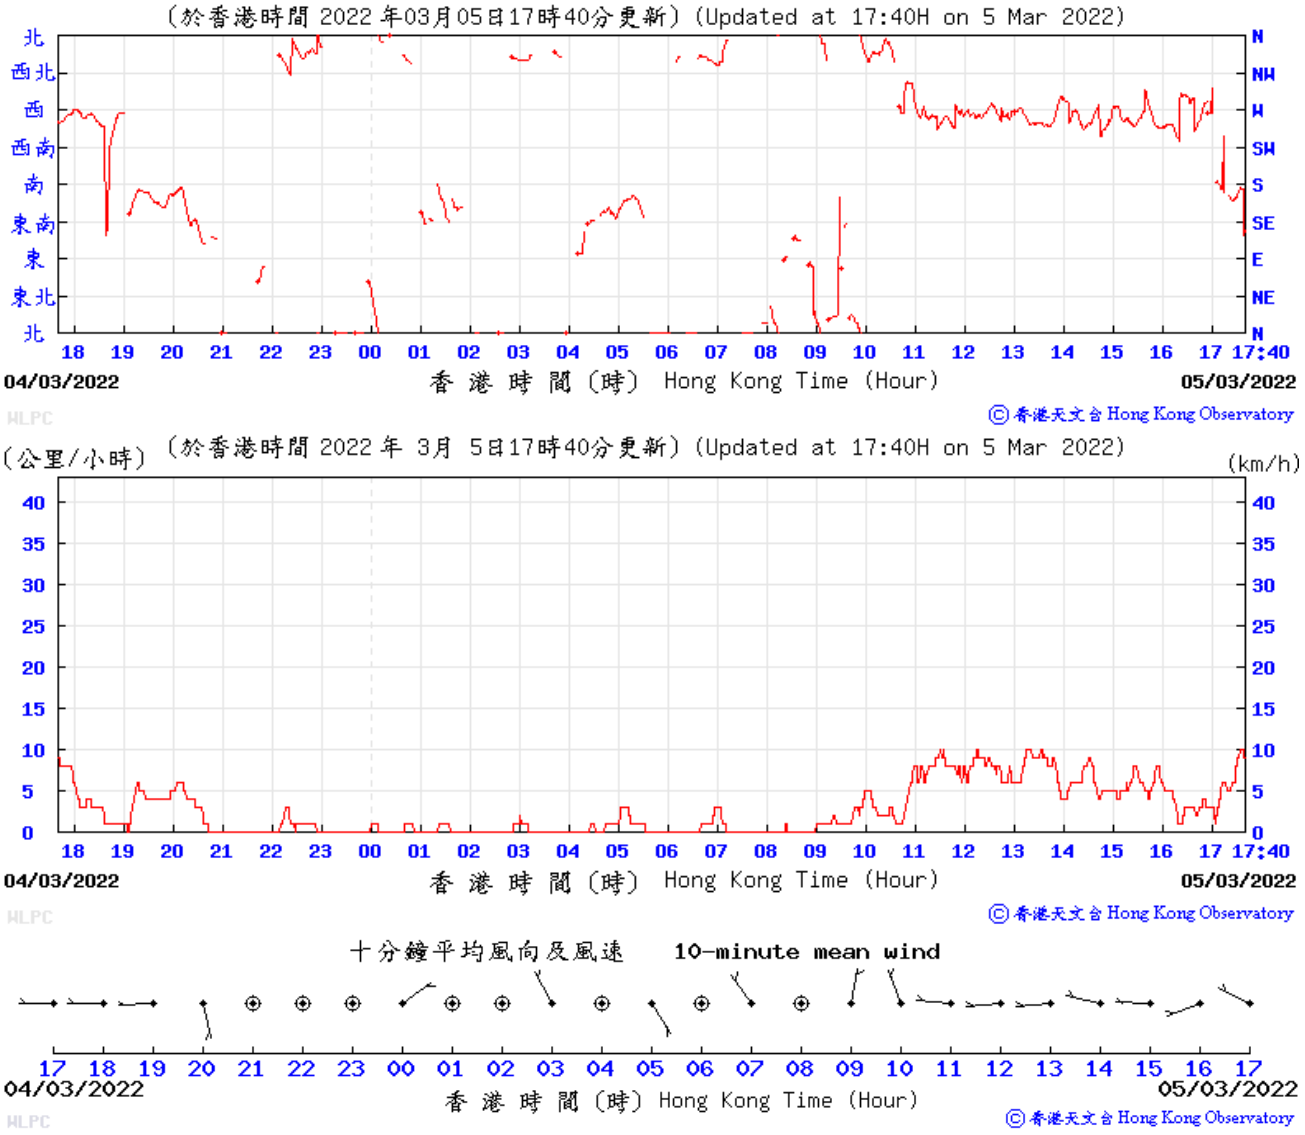

Wind Data for Wetland Park

10 March 2022

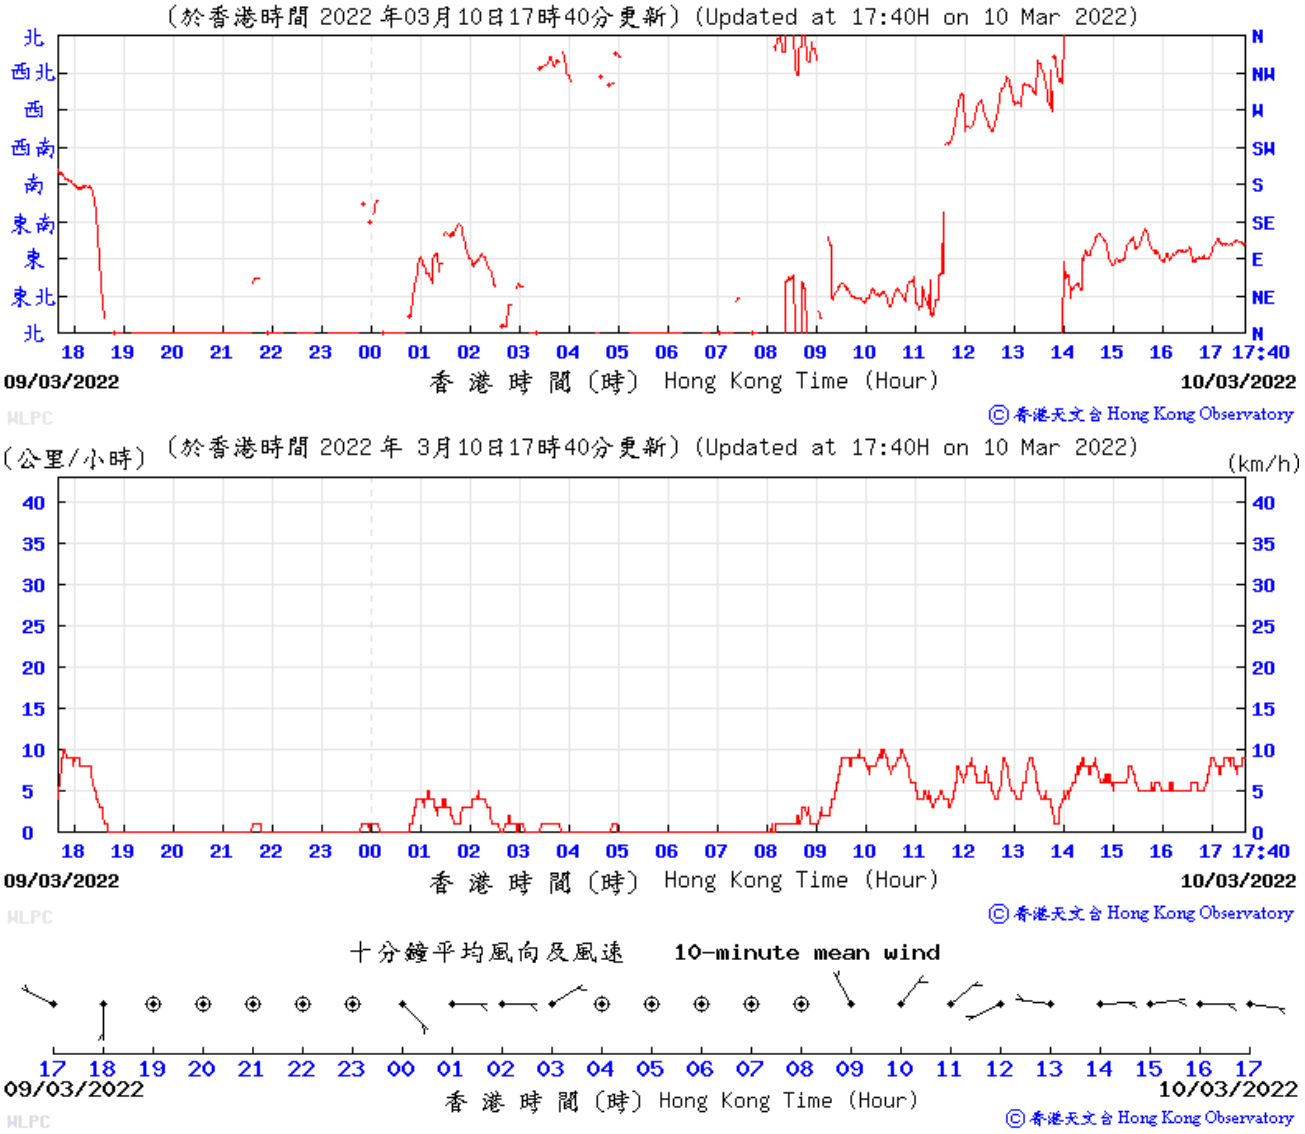

Wind Data for Wetland Park

11 March 2022

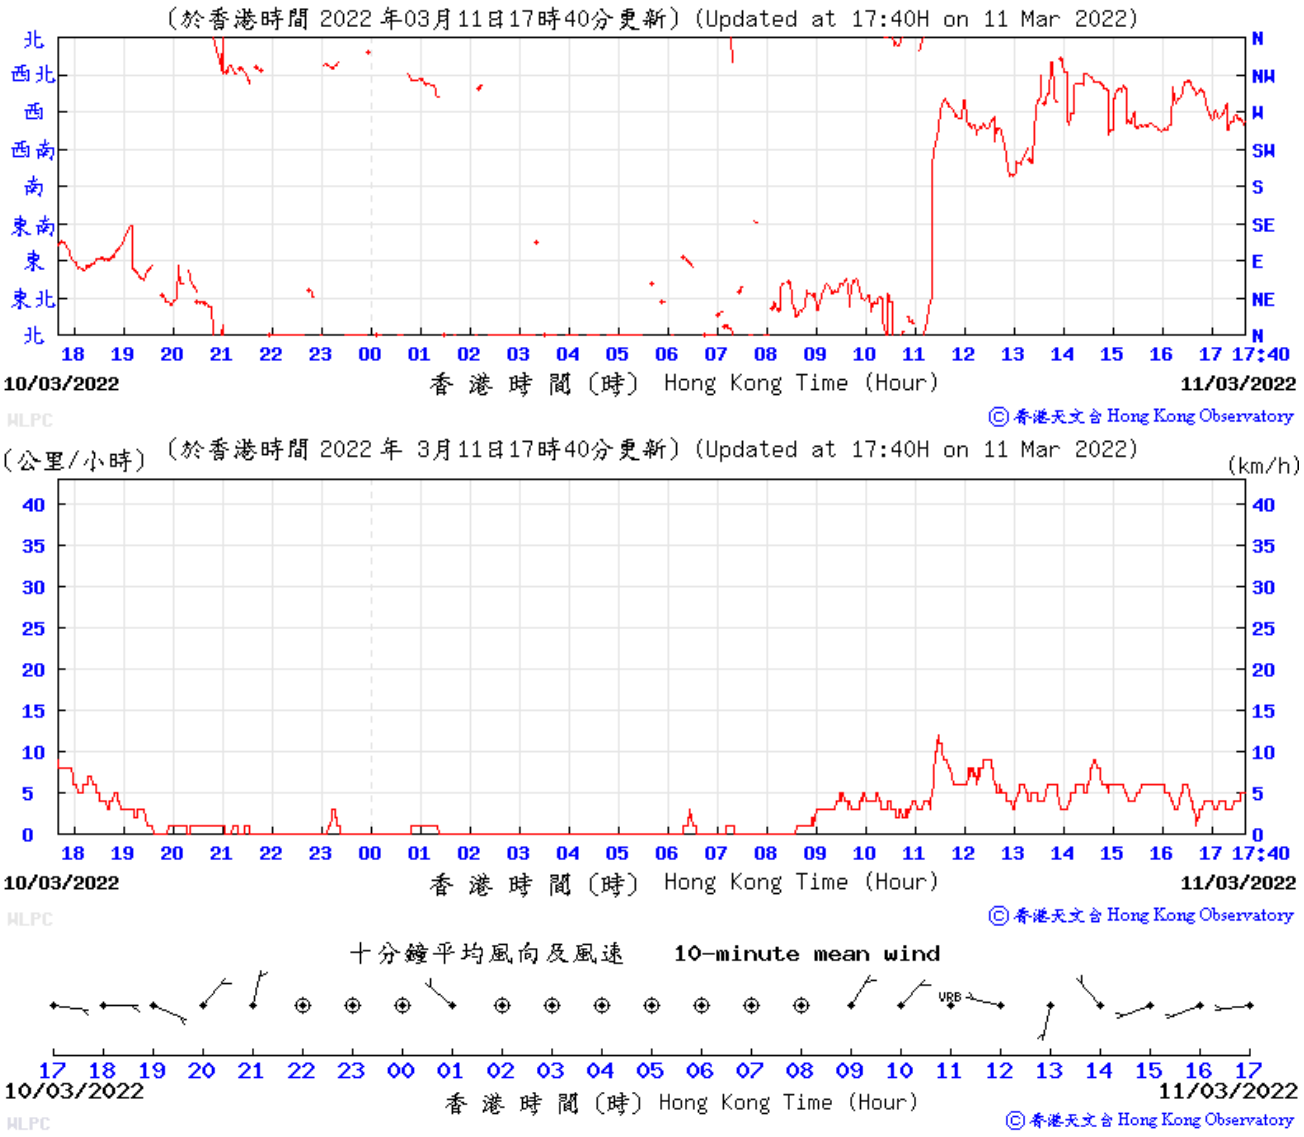

Wind Data for Wetland Park

16 March 2022

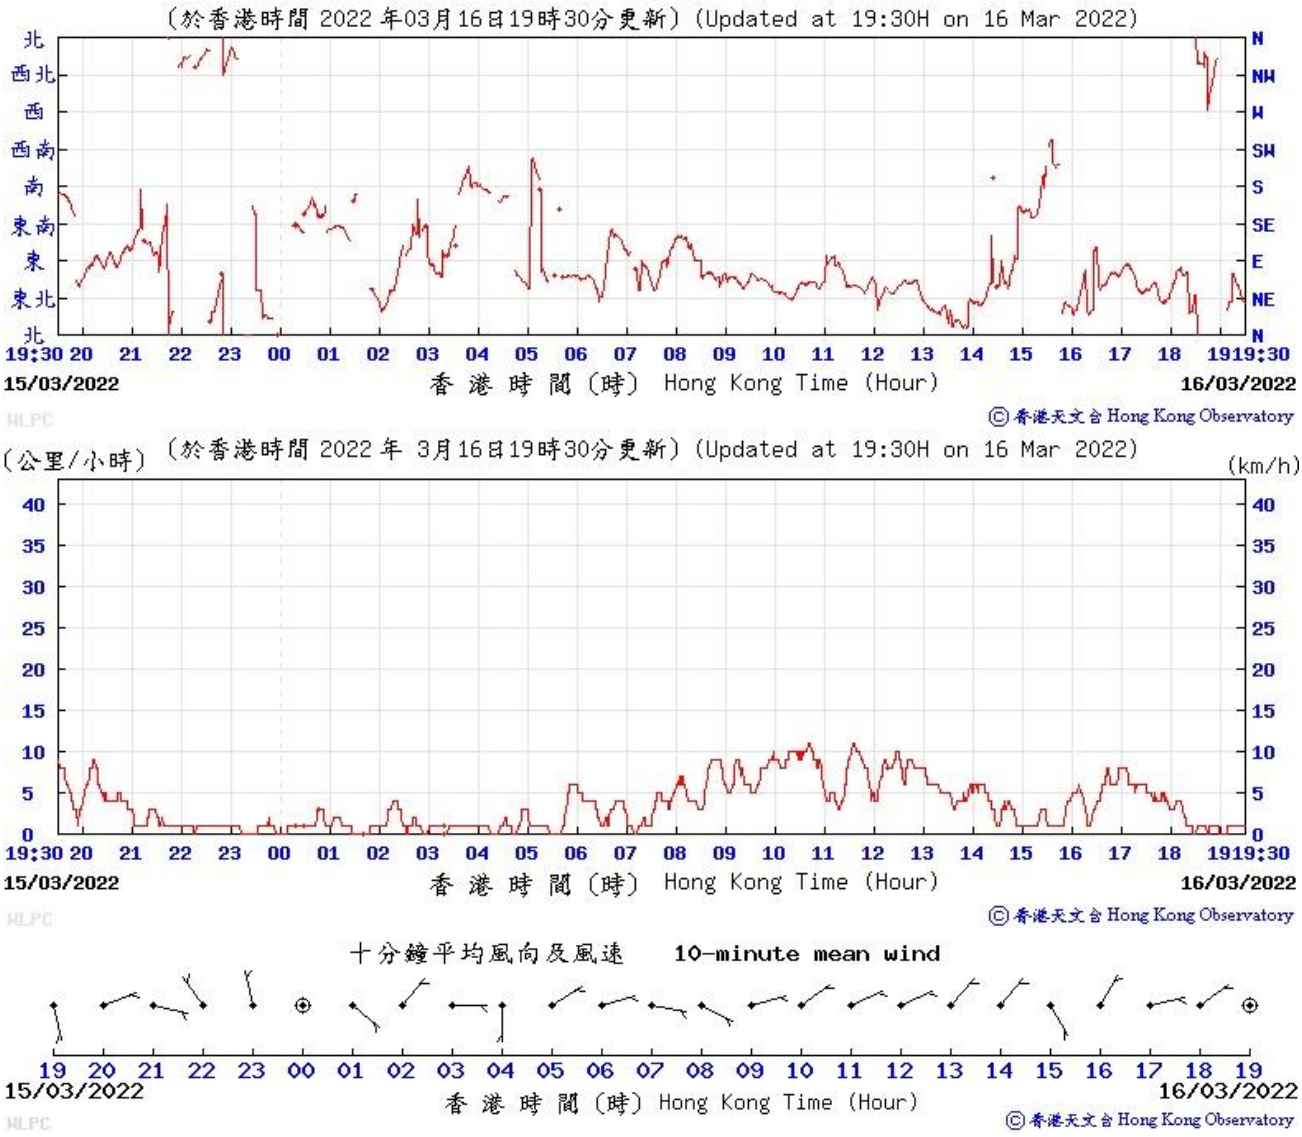

Wind Data for Wetland Park

17 March 2022

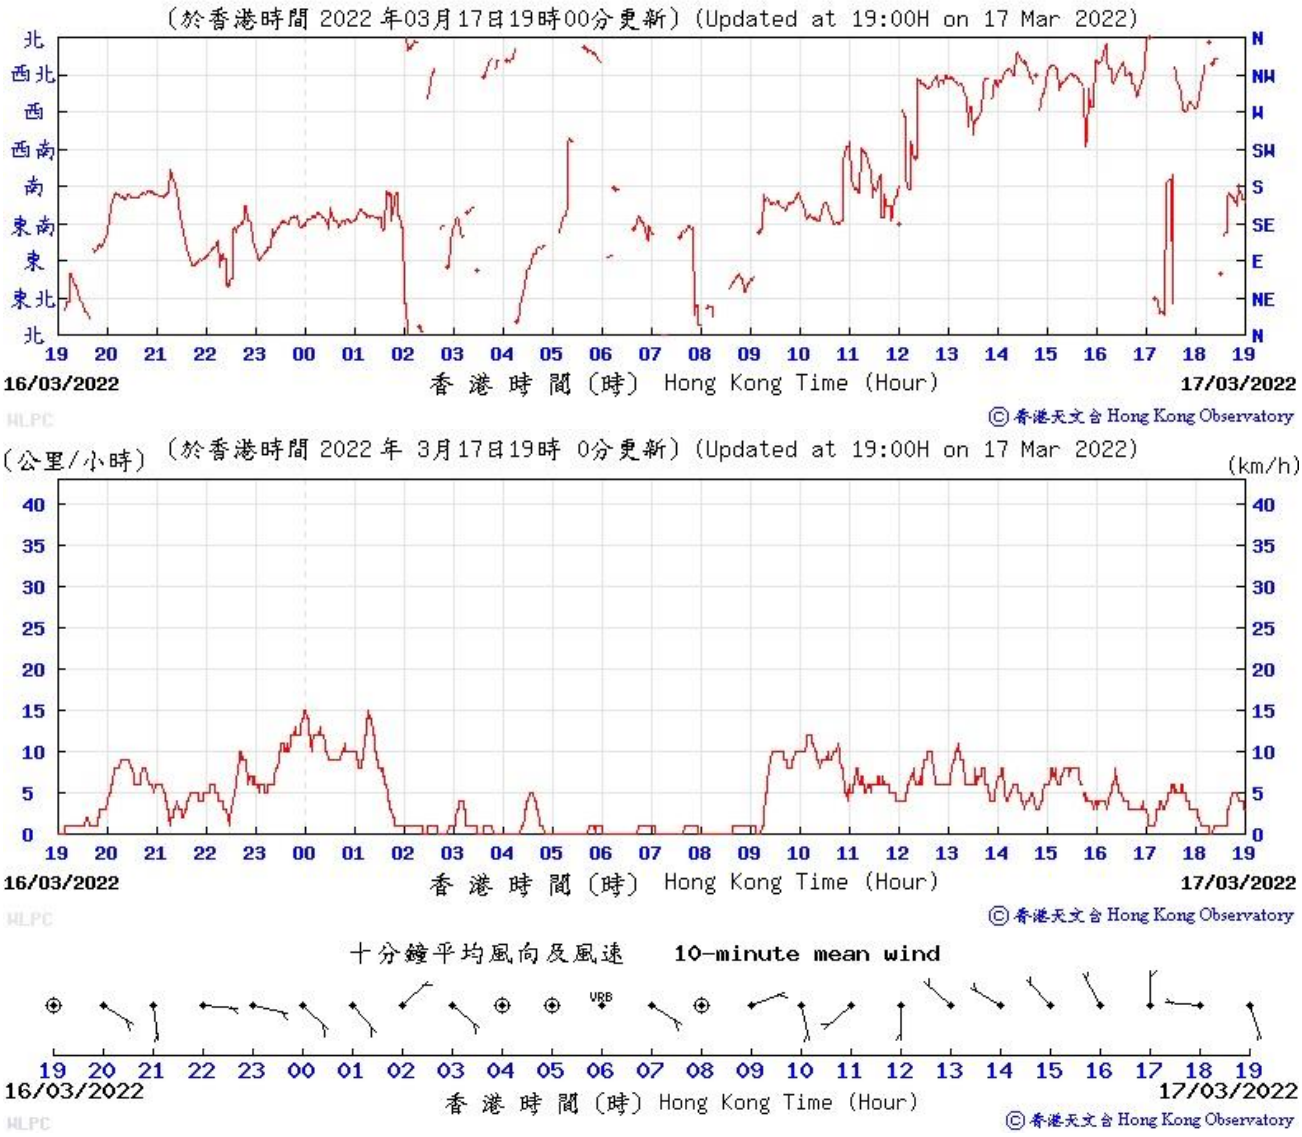

Wind Data for Wetland Park

22 March 2022

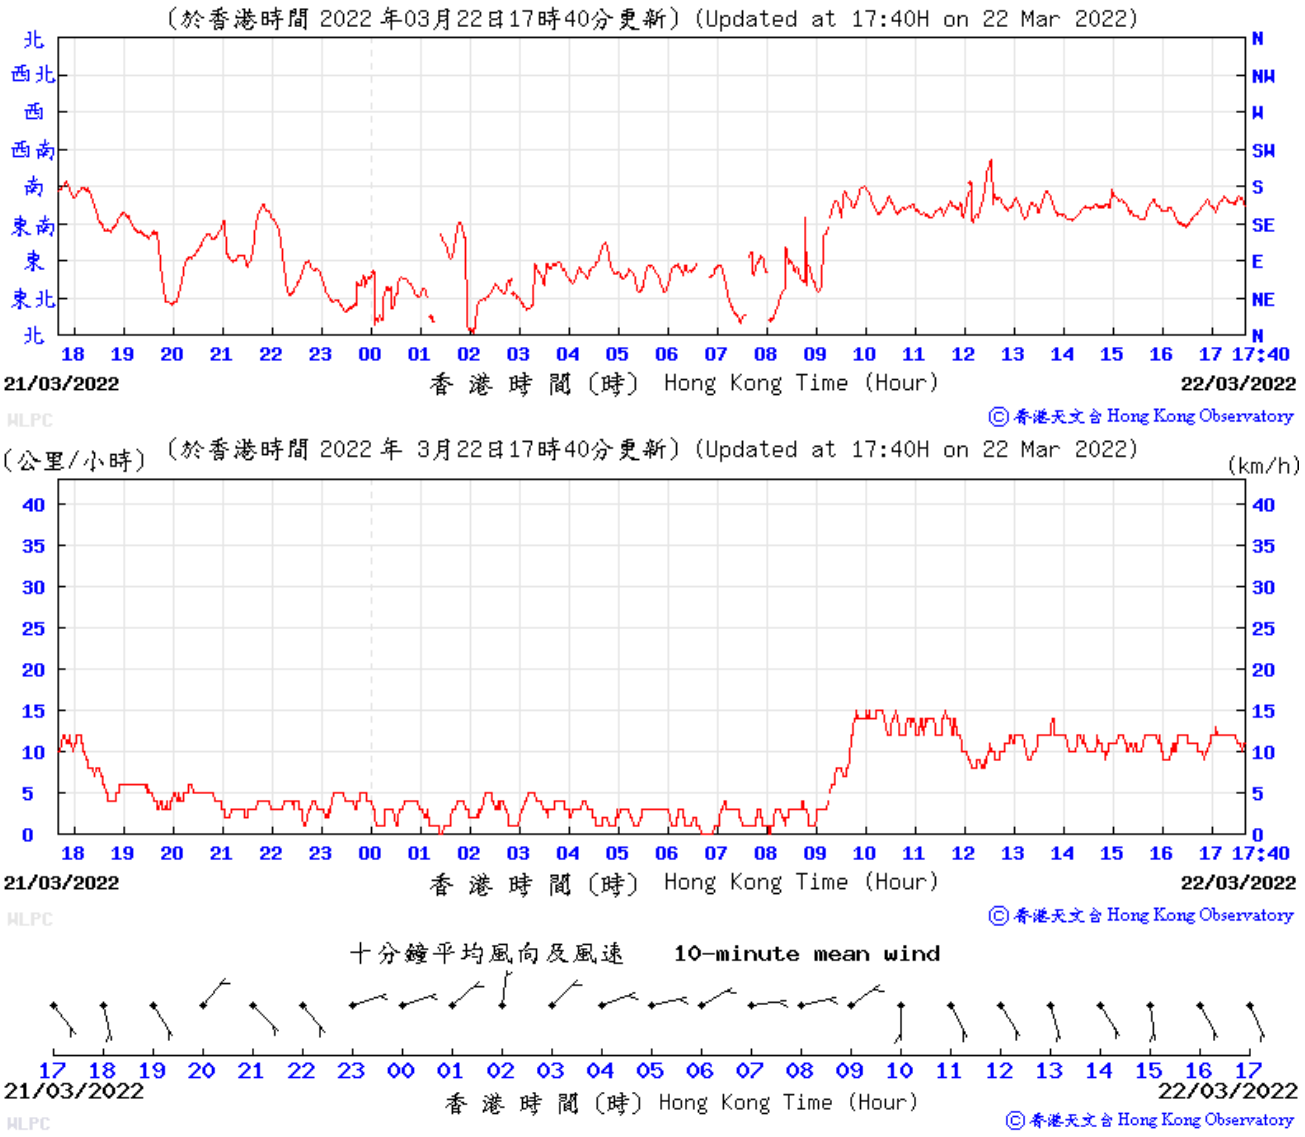

Wind Data for Wetland Park

23 March 2022

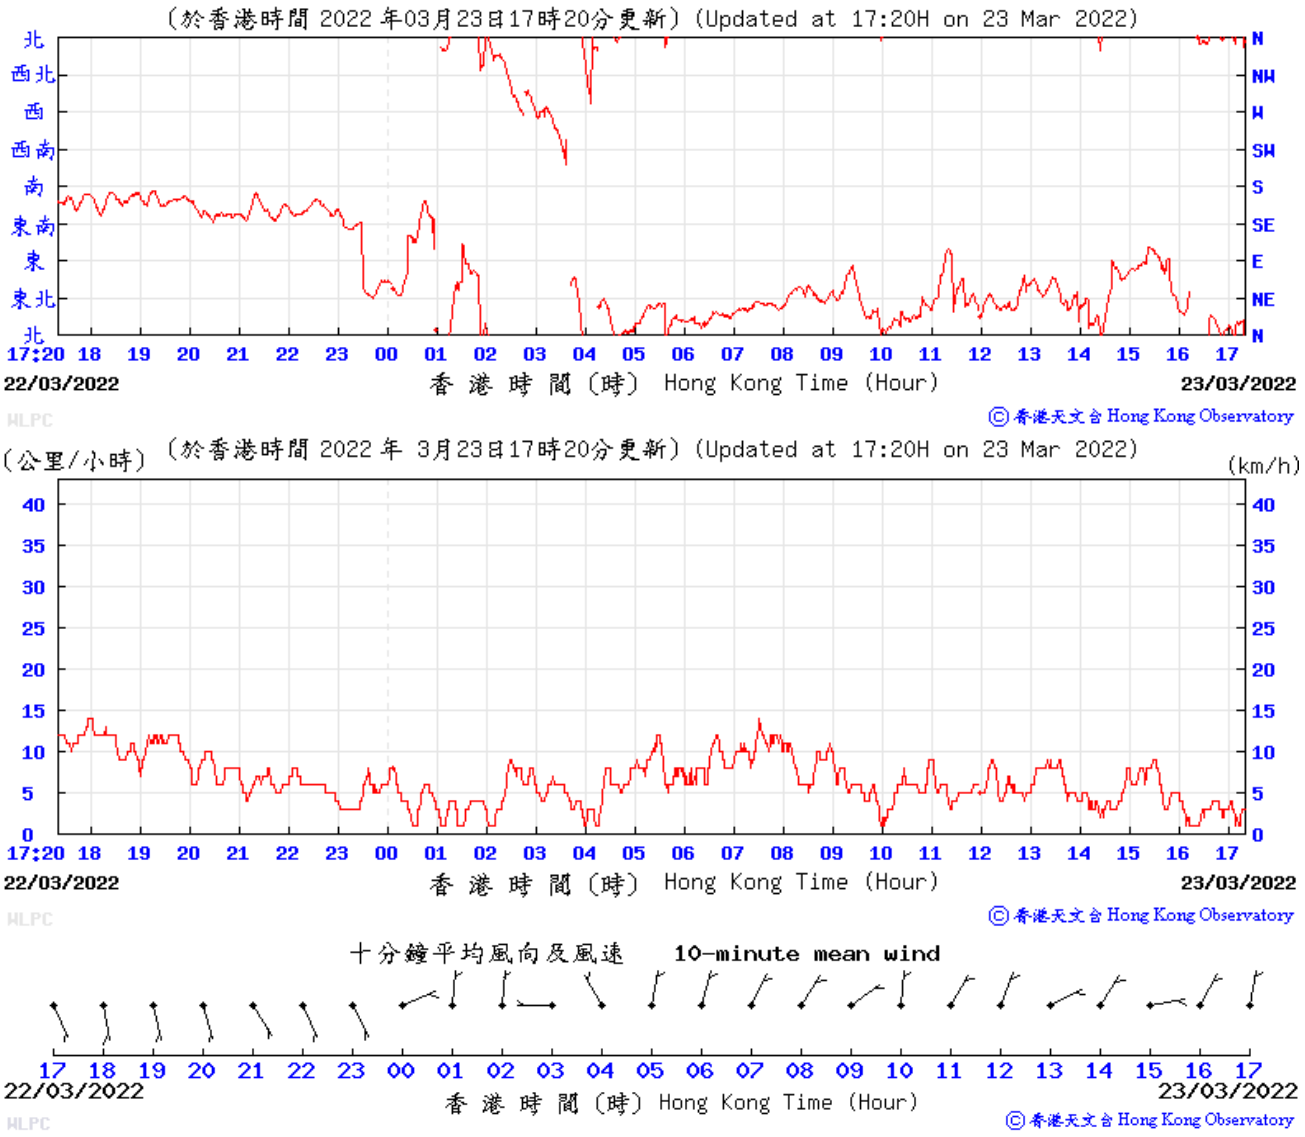

Wind Data for Wetland Park

28 March 2022

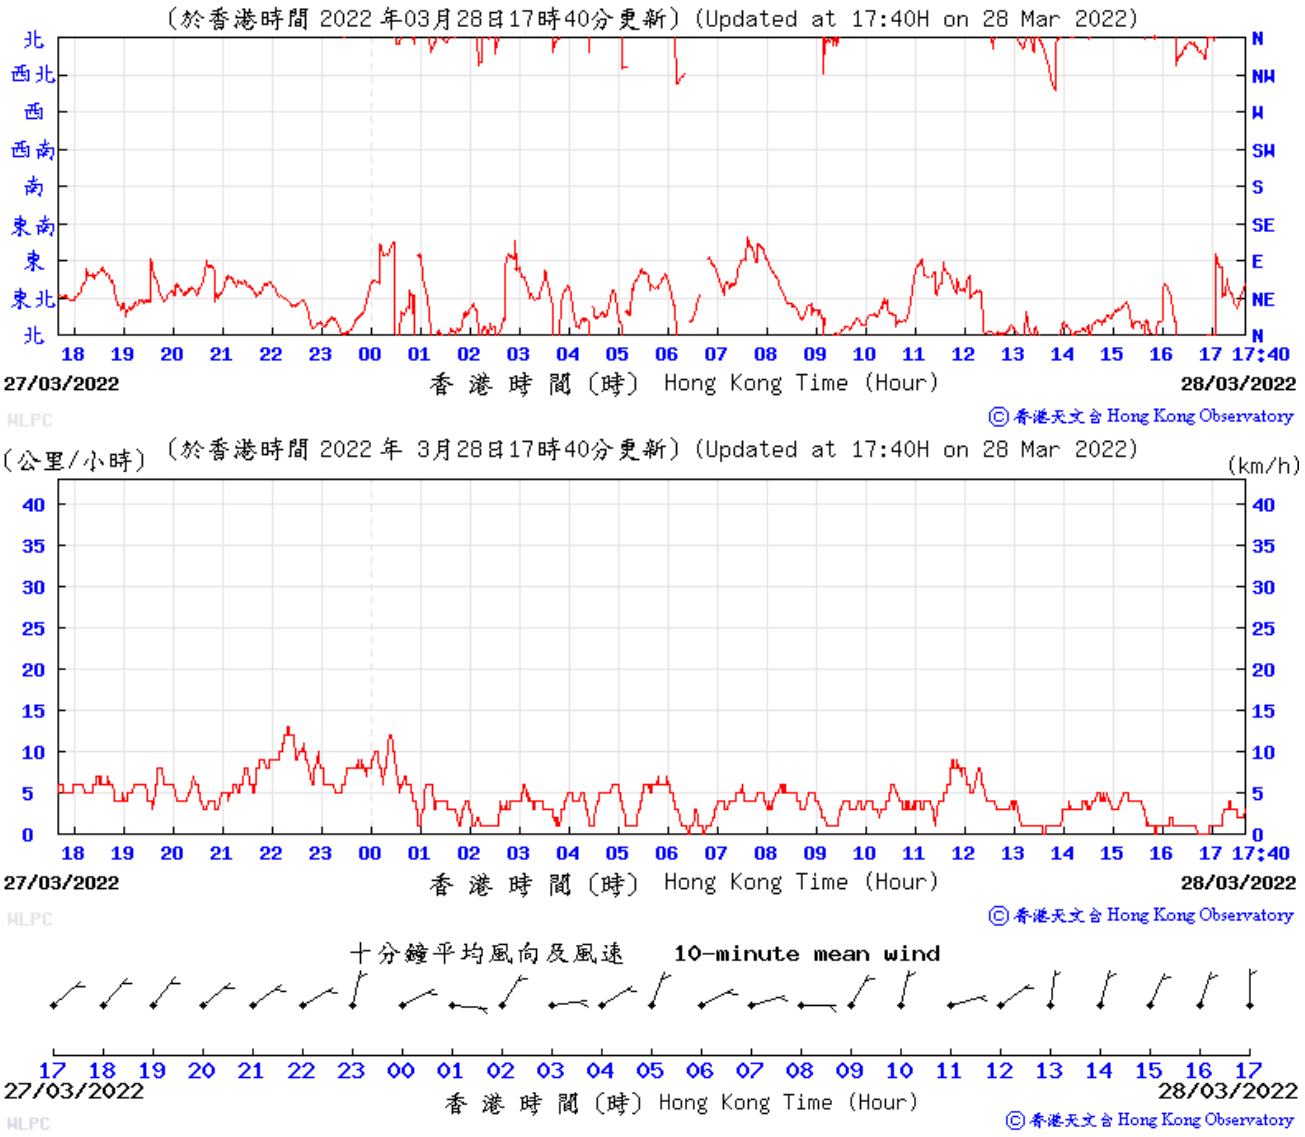

Wind Data for Wetland Park

29 March 2022

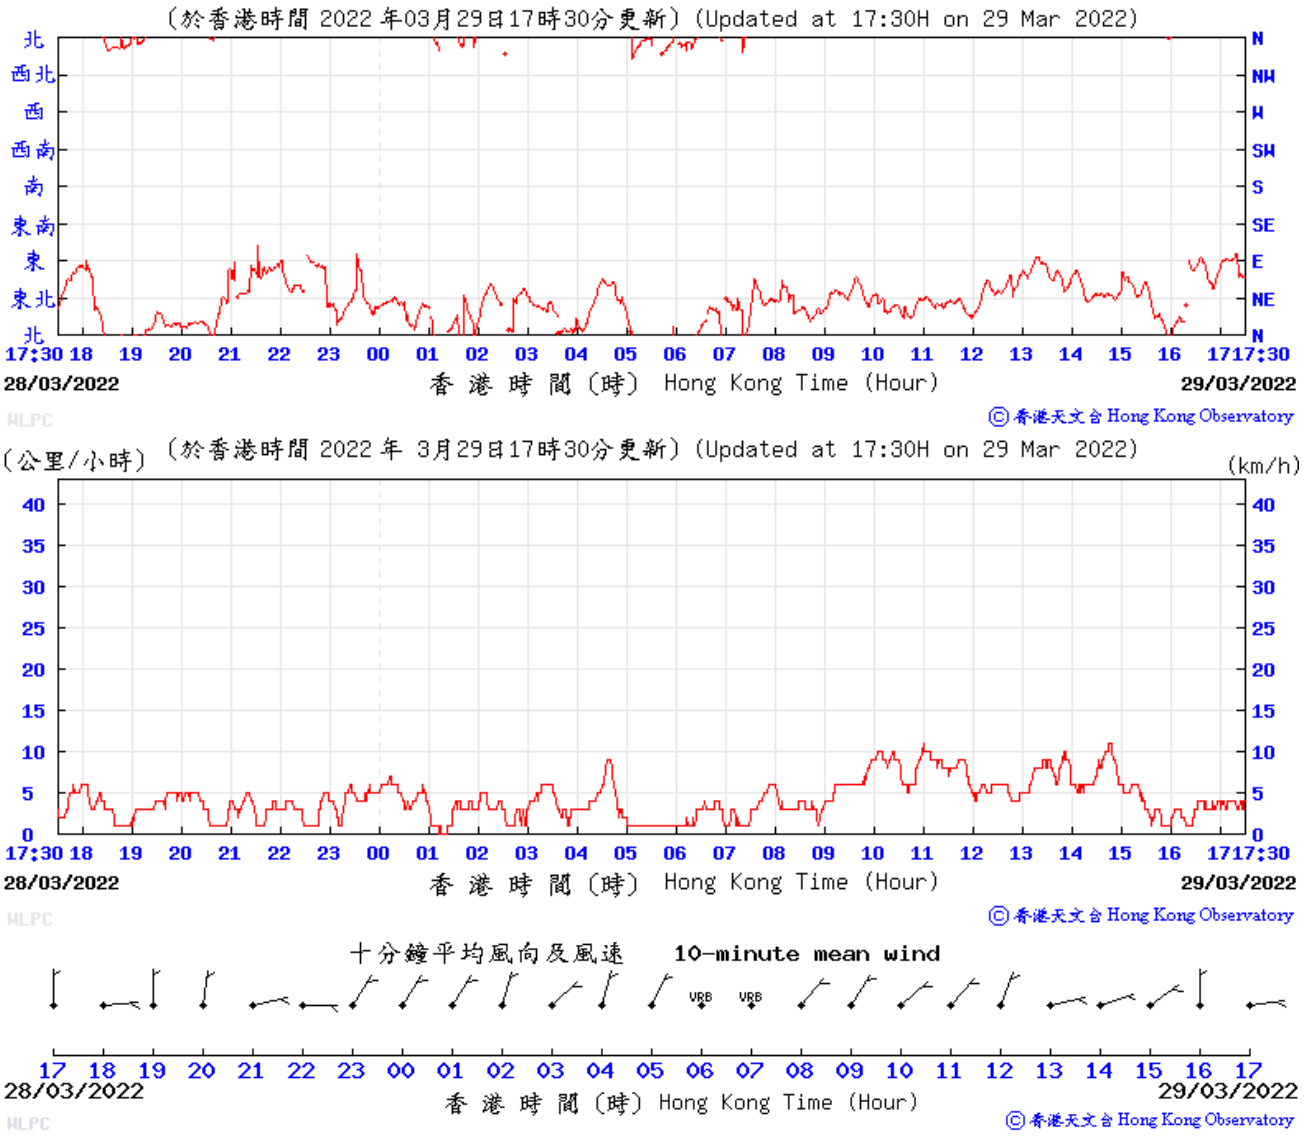

Wind Data for Lau Fau Shan

4 March 2022



Wind Data for Lau Fau Shan

5 March 2022

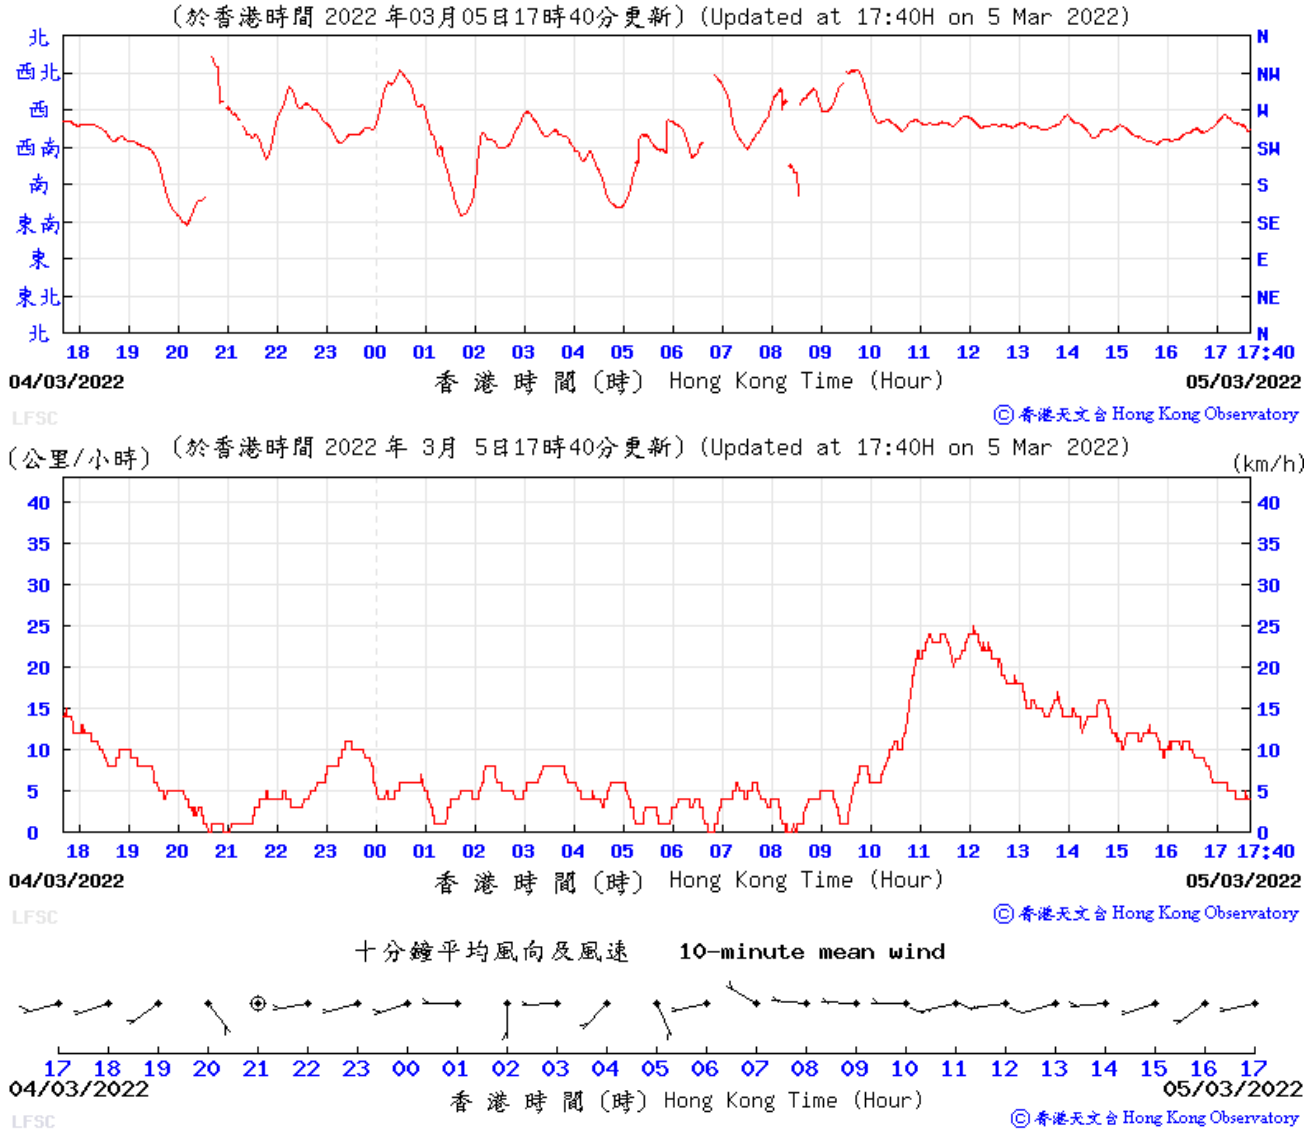

Wind Data for Lau Fau Shan

10 March 2022

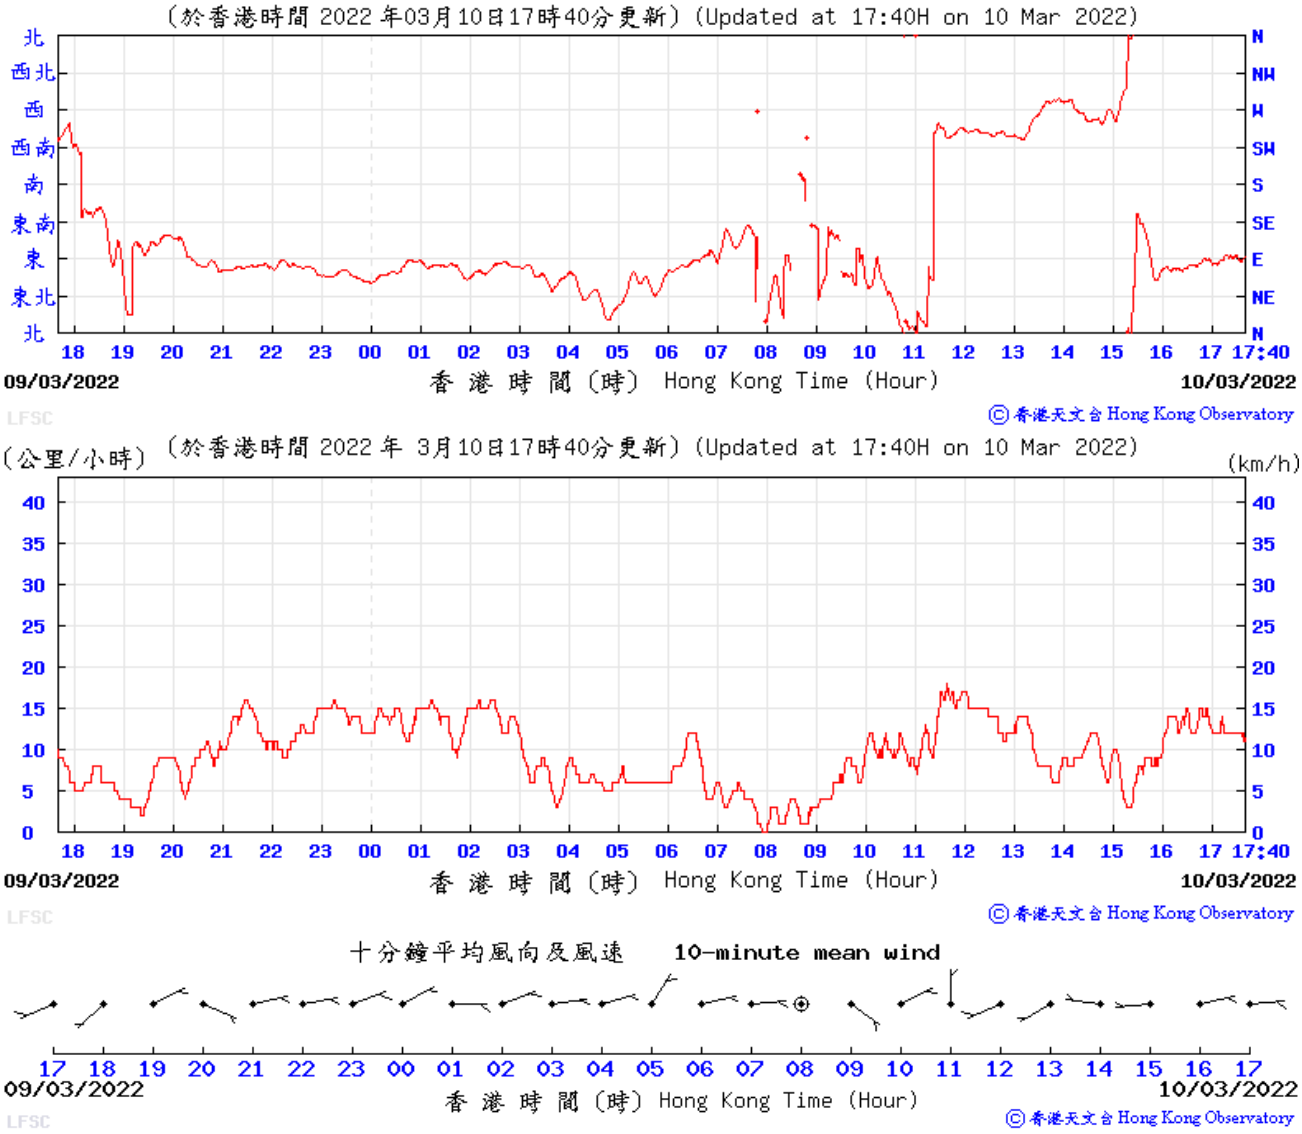

Wind Data for Lau Fau Shan

11 March 2022

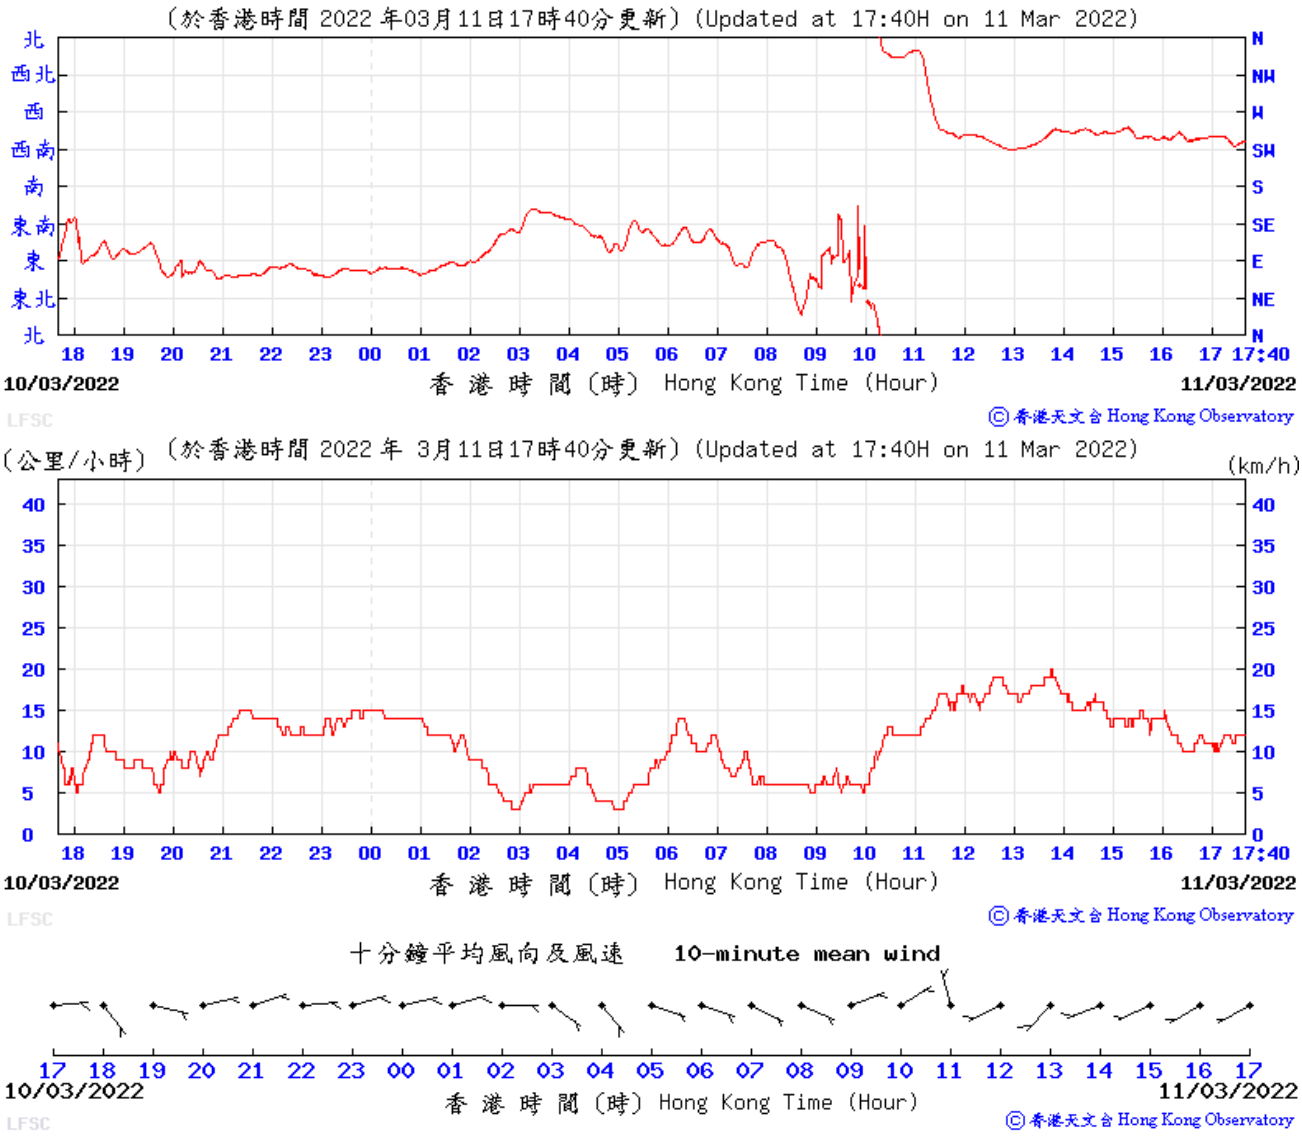

Wind Data for Lau Fau Shan

16 March 2022

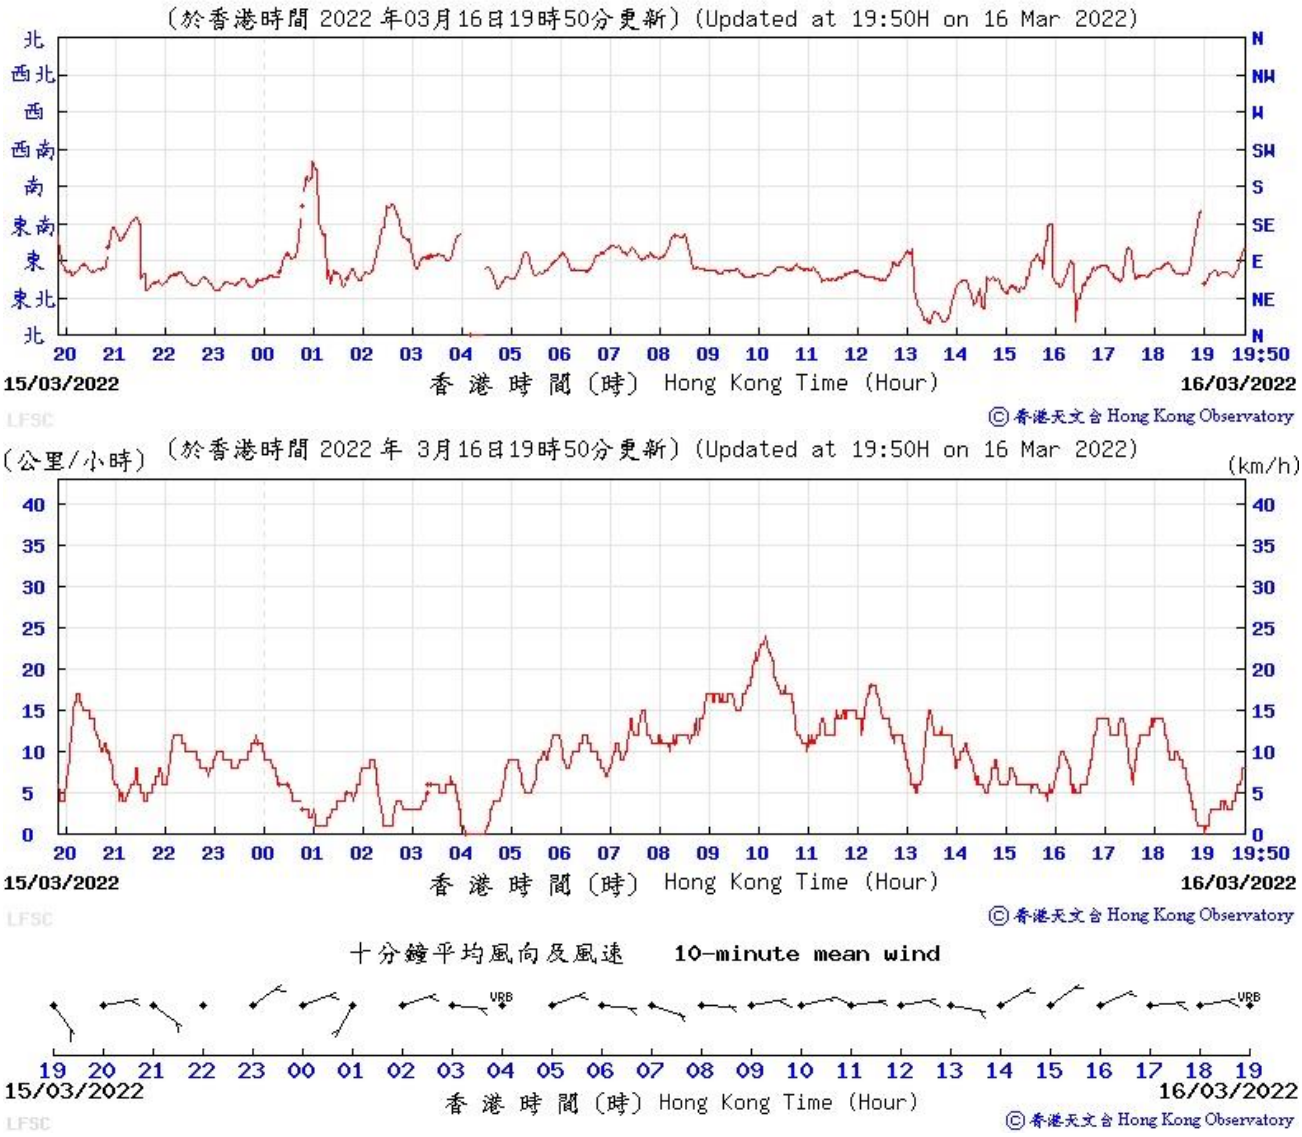

Wind Data for Lau Fau Shan

17 March 2022

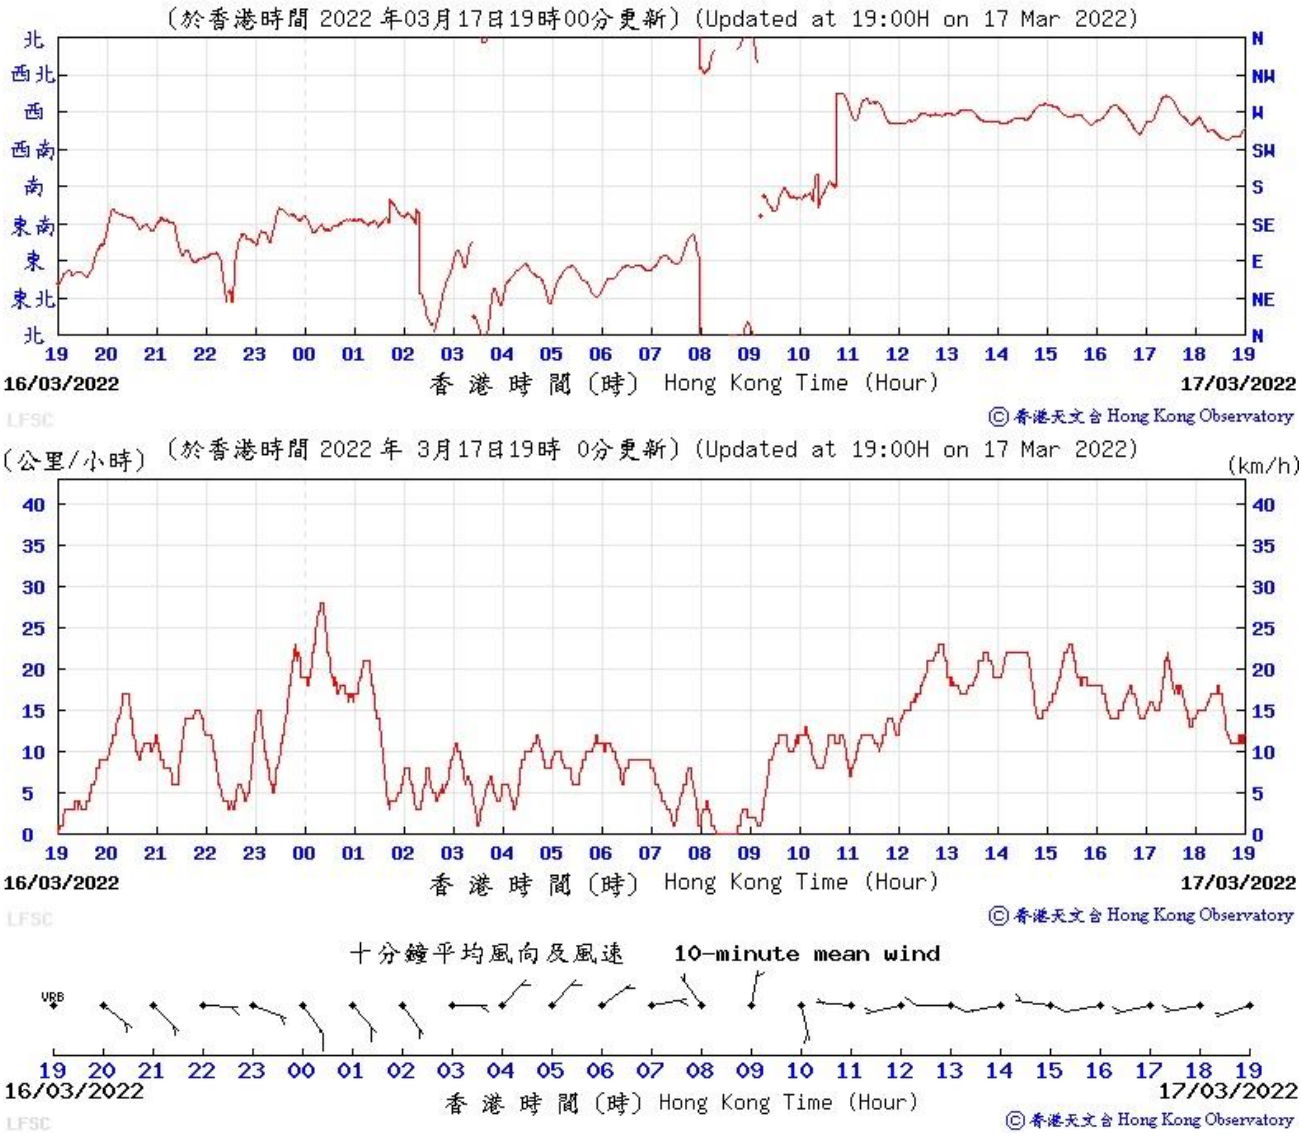

Wind Data for Lau Fau Shan

22 March 2022

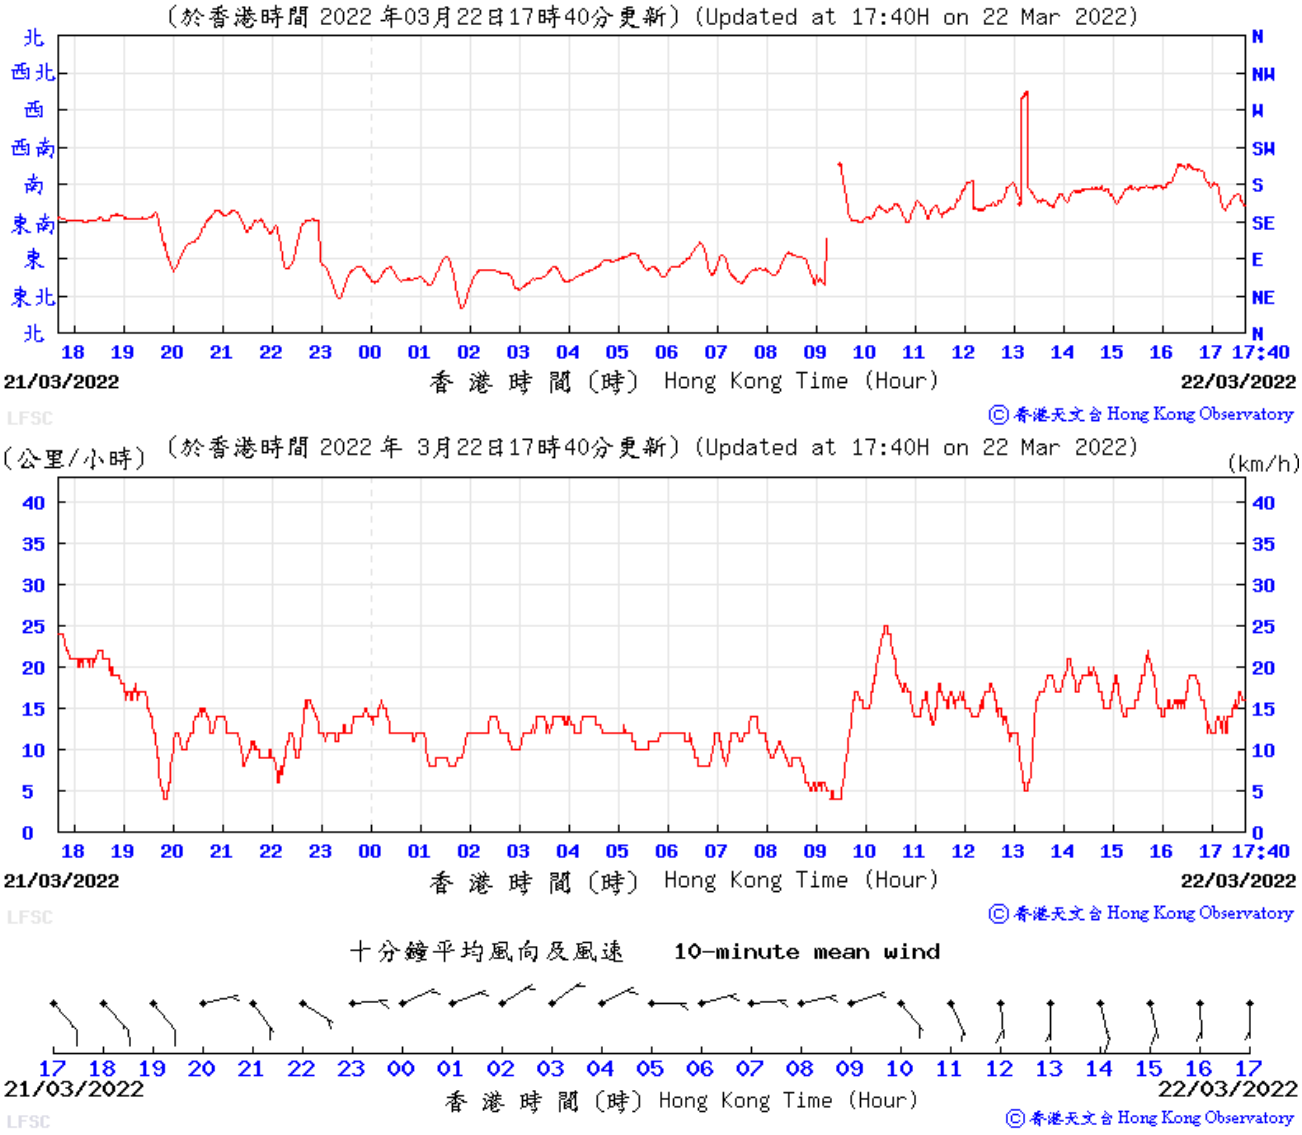

Wind Data for Lau Fau Shan

23 March 2022

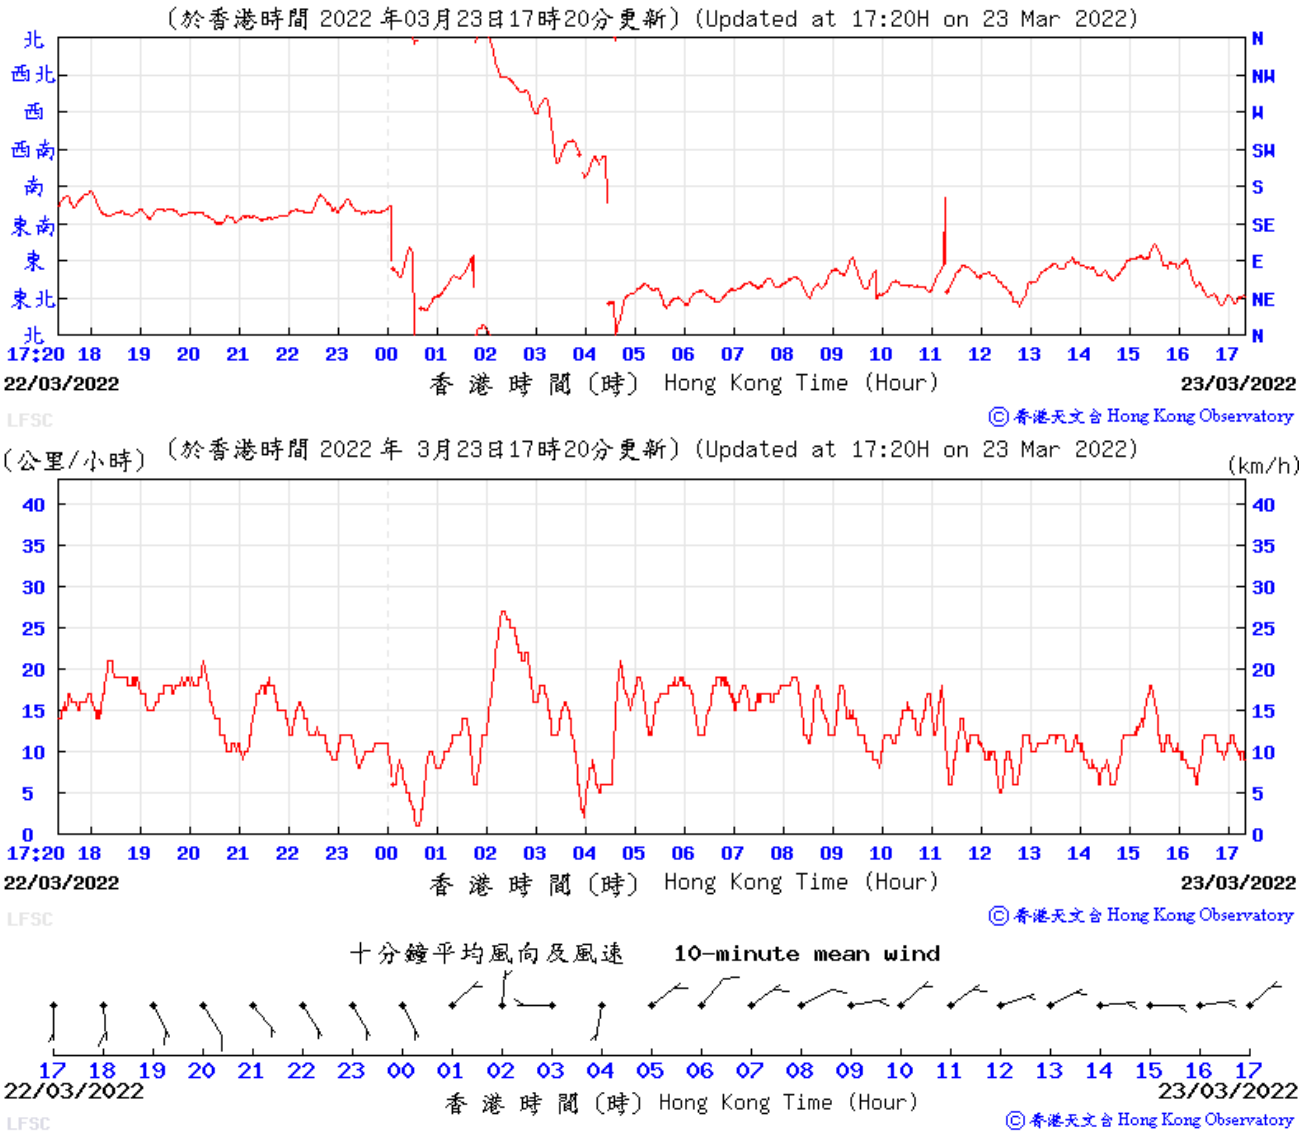

Wind Data for Lau Fau Shan

28 March 2022

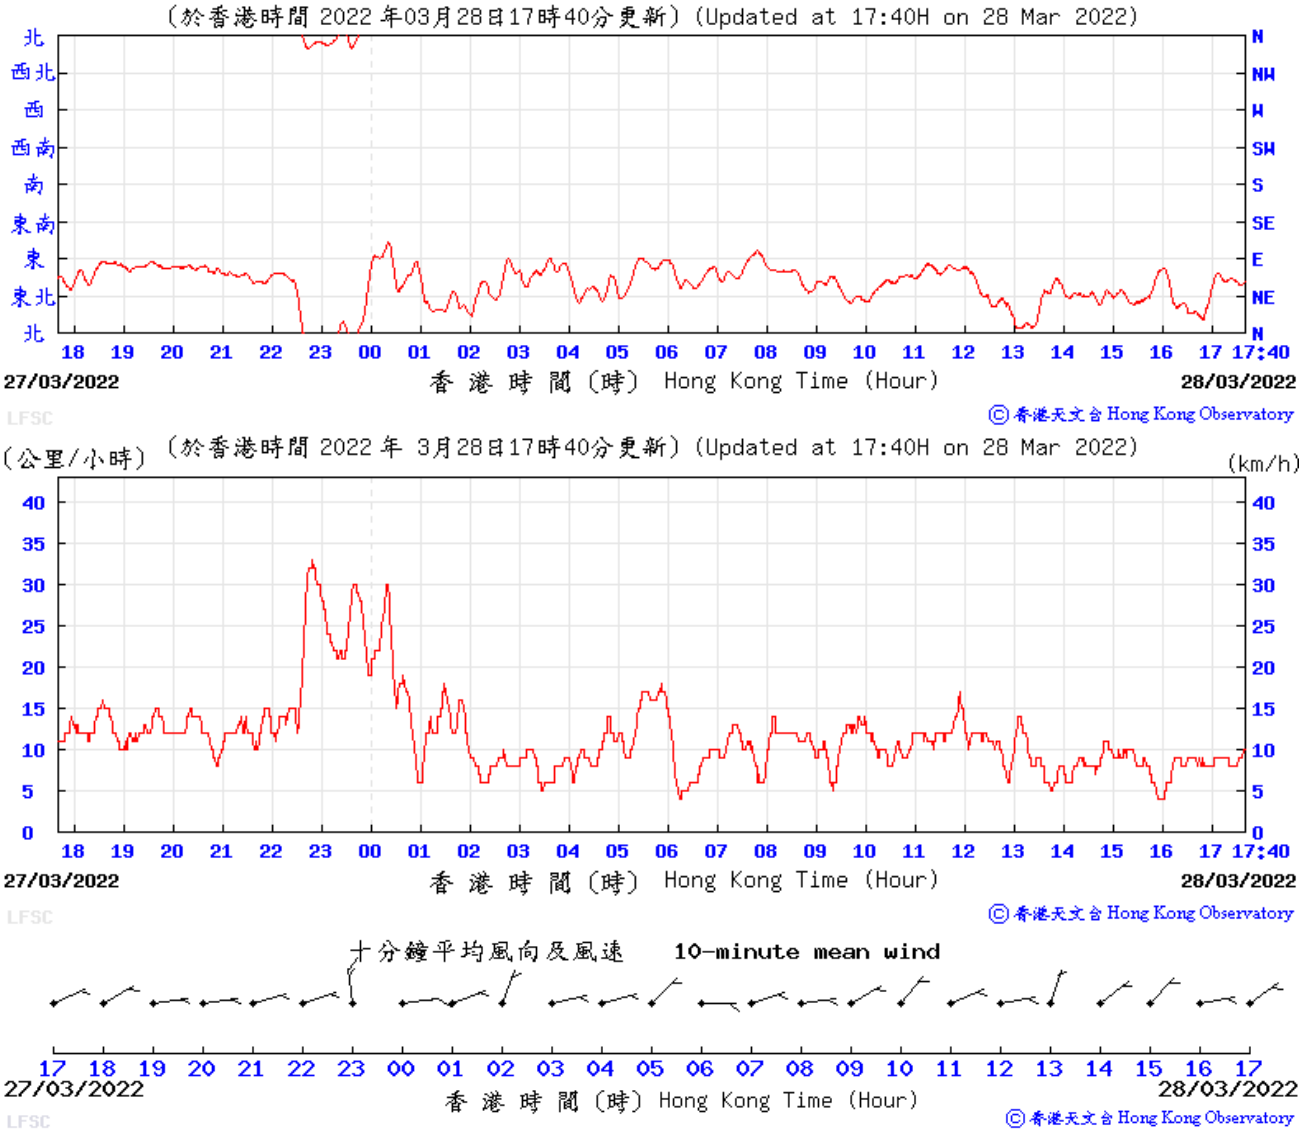

Wind Data for Lau Fau Shan

29 March 2022

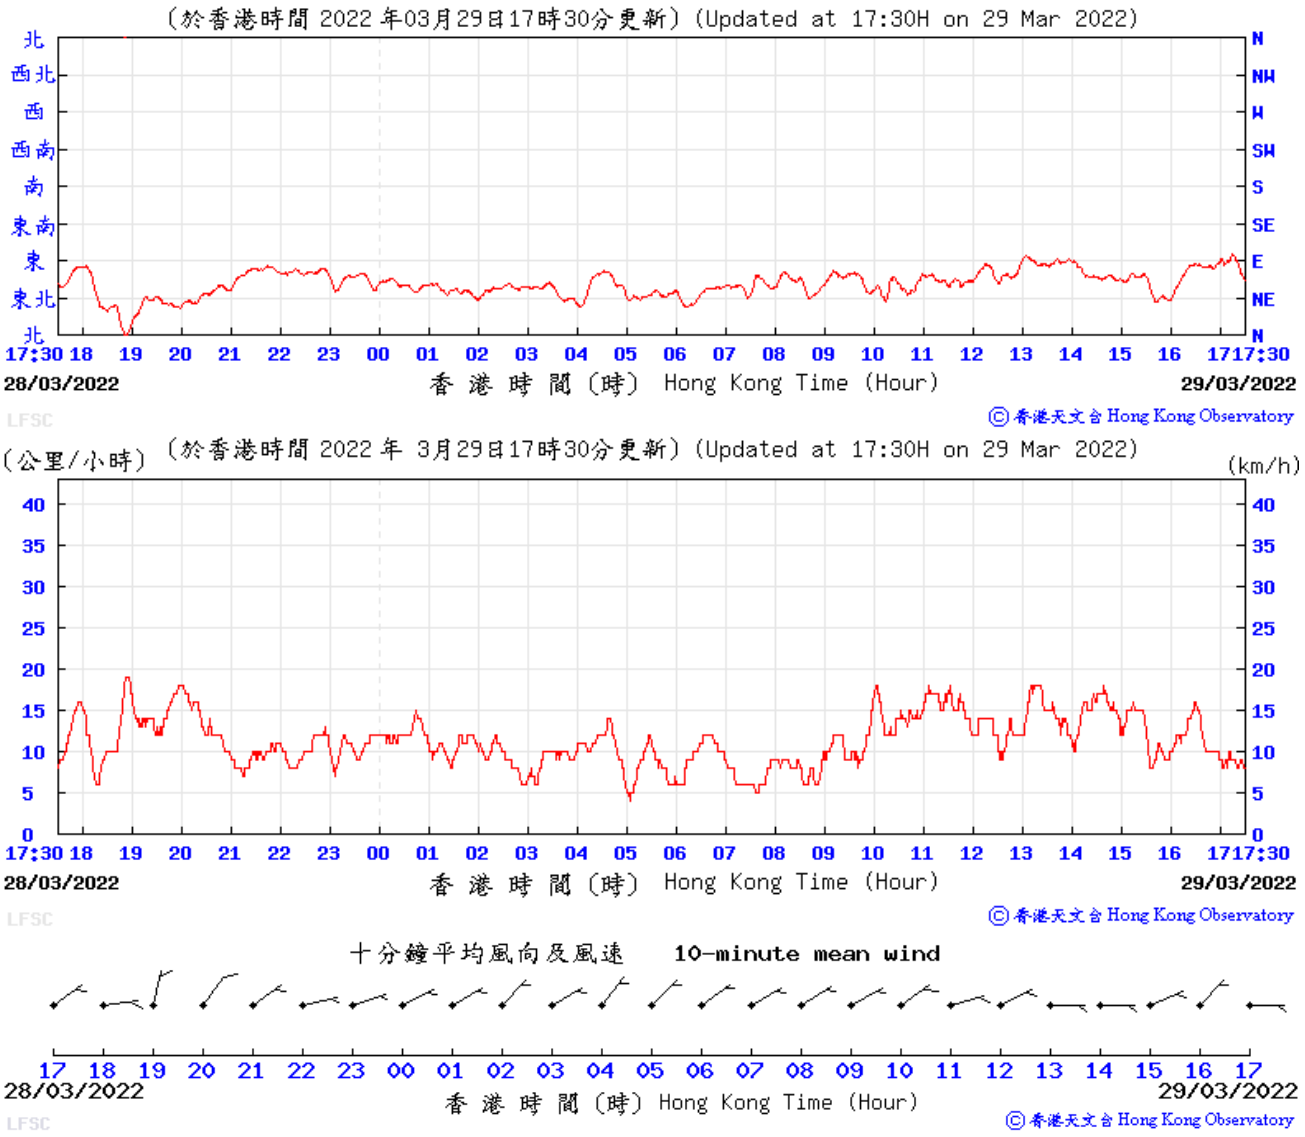

香港天文台 HONG KONG OBSERVATORY

Daily Extract

Daily Extract of Meteorological Observations , March 2022

Back Year 2022 Month 3 Go

Day	Hong Kong Observatory								King's Park	Waglan Island^	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mea Wir Spe (km
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
01	1016.9	26.3	22.0	19.1	17.6	77	56	0.0	***	***	**
02	1017.2	26.1	20.7	18.1	17.5	83	47	0.0	***	***	**
03	1017.2	22.6	19.5	17.4	15.0	76	56	0.0	***	***	**
04	1014.6	26.6	21.3	18.8	17.0	77	34	0.0	***	***	**
05	1013.5	24.6	20.6	17.9	17.8	84	39	0.0	***	***	**
06	1015.7	21.3	19.1	17.6	15.0	77	84	0.0	***	***	**
07	1017.2	24.6	19.8	16.8	13.6	70	62	4.8	***	***	**
08	1018.2	21.6	17.5	15.0	7.5	53	14	0.0	***	***	**
09	1017.2	24.3	18.7	15.1	9.7	57	14	0.0	***	***	**
10	1015.8	25.0	20.7	17.9	12.5	60	27	0.0	***	***	**
11	1014.0	26.9	22.1	18.8	16.5	71	40	0.0	***	***	**
12	1013.6	26.0	22.3	19.8	15.7	68	53	0.0	***	***	**
13	1012.8	27.7	23.6	21.0	18.8	75	47	0.1	***	***	**
14	1011.9	29.0	24.1	21.4	19.9	78	30	0.0	***	***	**
15	1010.8	28.4	23.8	21.1	19.9	80	43	0.0	***	***	**
16	1011.7	24.7	22.3	21.2	18.4	79	87	Trace	***	***	**
17	1009.4	27.7	24.3	22.1	21.5	85	79	Trace	***	***	**
18	1008.8	28.7	24.4	21.3	21.4	84	61	0.0	***	***	**
19	1009.9	25.8	23.3	22.3	20.6	85	75	0.0	***	***	**
20	1012.6	22.9	21.0	19.9	18.9	88	88	Trace	***	***	**
21	1012.9	23.7	22.1	21.0	20.2	89	88	Trace	***	***	**
22	1012.8	25.1	23.0	21.2	21.7	93	95	Trace	***	***	**
23	1014.7	21.6	17.7	16.3	16.6	94	91	54.8	***	***	**

24	1014.3	18.5	17.6	16.3	16.1	91	93	1.8	***	***	**
25	1010.4	26.7	23.1	18.1	21.3	90	92	0.7	***	***	**
26	1010.4	28.7	26.4	24.9	23.9	86	88	0.1	***	***	**
27	1013.4	25.4	21.9	19.1	18.9	83	88	Trace	***	***	**
28	1017.4	19.2	17.5	16.4	15.6	89	88	30.3	***	***	**
29	1017.2	21.2	19.1	17.4	15.8	82	86	0.1	***	***	**
30	1015.9	26.1	22.4	19.5	17.5	74	82	0.0	***	***	**
31	1016.3	29.3	24.4	21.9	18.2	69	56	Trace	***	***	**
Mean/Total	1014.0	25.0	21.5	19.2	17.4	79	64	92.7	***	***	**
Climatological Normal[?]	1016.1	21.9	19.5	17.6	16.1	82	77	75.3	100.0	060	23.

*** *unavailable*

^ *Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since August 1989*

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

H. Ecological Monitoring conducted

March 2022	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
Mammals			✓							✓					✓
Birds			✓							✓					
Herpetofauna															✓(d)
Dragonflies & butterflies															
Water Quality															+
Inspection Visits		✓								✓					✓
Vegetation and Exotic Species Control		✓												✓	

March 2022	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
Mammals		✓✓				✓								✓✓		
Birds		✓				✓								✓		
Herpetofauna														✓(n)		
Dragonflies & butterflies		✓														
Water Quality							✓							+		
Inspection Visits						✓								✓		
Vegetation and Exotic Species Control						✓									✓	

Notes:
Light grey cells indicate public holidays, Saturdays or Sundays
"d" and "n" indicate daytime and night-time herpetofauna surveys respectively
+ indicates water level monitoring
# indicates additional pH level monitoring
@ indicates extra water quality monitoring

I. Summary of Bird Surveys conducted

Table I1: Summary of bird species of conservation importance and/or wetland-dependence recorded in the Survey Area (excluding the WRA)

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]	Mar 2022 Occurrence[3]	Mar 2022 Mean[4]	Records outside surveys[5]
Little Grebe	*Tachybaptus ruficollis*	Y	LC	5	16.0	0
Great Cormorant	*Phalacrocorax carbo*	Y	PRC	4	63.0	0
Grey Heron	*Ardea cinerea*	Y	PRC	3	8.0	0
Great Egret	*Ardea alba*	Y	PRC, (RC)	5	6.6	0
Little Egret	*Egretta garzetta*	Y	PRC, (RC)	5	34.6	0
Eastern Cattle Egret	*Bubulcus coromandus*	Y	(LC)	1	1.6	0
Chinese Pond Heron	*Ardeola bacchus*	Y	PRC, (RC)	5	14.2	0
Black-crowned Night Heron	*Nycticorax nycticorax*	Y	(LC)	-	-	V
Black-faced Spoonbill##	*Platalea minor*	Y	Class I, PGC, EN	4	4.8	0
Tufted Duck	*Aythya fuligula*	Y	LC	3	6.6	0
Black Kite#	*Milvus migrans*	Y	Class II, (RC)	2	0.6	0
Eastern Buzzard#	*Buteo japonicus*	Y	Class II	1	0.2	0
White-breasted Waterhen	*Amaurornis phoenicurus*	Y	-	5	2.4	0
Common Moorhen	*Gallinula chloropus*	Y	-	2	0.6	0
Black-winged Stilt	*Himantopus himantopus*	Y	RC	3	8.8	0
Pied Avocet	*Recurvirostra avosetta*	Y	RC	2	1.0	0
Little Ringed Plover	*Charadrius dubius*	Y	(LC)	2	0.6	0
Common Redshank	*Tringa totanus*	Y	RC	1	0.2	0
Common Greenshank	*Tringa nebularia*	Y	RC	2	0.4	0
Green Sandpiper	*Tringa ochropus*	Y	-	3	0.8	0
Wood Sandpiper	*Tringa glareola*	Y	LC	3	2.4	0
Common Sandpiper	*Actitis hypoleucos*	Y	-	5	4.2	0
Pied Kingfisher	*Ceryle rudis*	Y	(LC)	4	1.8	0
White-throated Kingfisher#	*Halcyon smyrnensis*	Y	Class II, (LC)	1	0.4	0
Common Kingfisher	*Alcedo atthis*	Y	-	5	1.8	0
Eastern Yellow Wagtail	*Motacilla tschutschensis*	Y	-	5	8.2	0

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]	Mar 2022 Occurrence[3]	Mar 2022 Mean[4]	Records outside surveys[5]
Grey Wagtail	*Motacilla cinerea*	Y	-	1	0.2	0
White Wagtail	*Motacilla alba*	Y	-	5	6.6	0
Red-throated Pipit	*Anthus cervinus*	N	LC	1	0.4	0
Zitting Cisticola	*Cisticola juncidis*	Y	LC	2	1.0	0
White-shouldered Starling	*Sturnia sinensis*	Y	(LC)	3	1.2	0
Collared Crow	*Corvus torquatus*	Y	LC, NT	2	1.0	0
			No. of species recorded:	**32**		

Note:
(1) Follows HK bird list (dated 2020-03).
(2) Conservation status follows that of Fellowes *et al*. (2002) and BirdLife International listing (2017). Letters in parentheses indicate that the assessment is on the basis of restrictedness in breeding and/or roosting sites rather than in general occurrence. (Fellowes *et al*. 2002)
(3) Indicates number of surveys recorded within the reporting period.
(4) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA).
(5) Includes observations during other surveys and/or site visits.
(6) Five regular surveys and three outside surveys were conducted
Birds tagged with '#' are Category II protected under terrestrial wildlife state protection
Birds tagged with '##" are Category I protected under terrestrial wildlife state protection
V Indicates the species is recorded outside regular surveys

Table I2: Summary of bird species of conservation importance and/or wetland-dependence recorded in the WRA

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]	Mar 2022 Occurrence[3]	Mar 2022 Mean[4]	Records outside surveys[5]
Little Grebe	*Tachybaptus ruficollis*	Y	LC	1	0.2	0
Great Cormorant	*Phalacrocorax carbo*	Y	PRC	1	0.2	0
Grey Heron	*Ardea cinerea*	Y	PRC	1	0.2	0
Great Egret	*Ardea alba*	Y	PRC, (RC)	4	2.2	0
Little Egret	*Egretta garzetta*	Y	PRC, (RC)	4	1.6	0
Chinese Pond Heron	*Ardeola bacchus*	Y	PRC, (RC)	3	1.0	0
Great Bittern	*Botaurus stellaris*	Y	RC	1	0.2	0
Black-crowned Night Heron	*Nycticorax nycticorax*	Y	(LC)	-	-	V
Black Kite#	*Milvus migrans*	Y	Class II, (RC)	3	0.6	0
Eastern Buzzard#	*Buteo japonicus*	Y	Class II	1	0.2	0
White-breasted Waterhen	*Amaurornis phoenicurus*	Y	-	3	2.2	0
Common Moorhen	*Gallinula chloropus*	Y	-	5	2.0	0
Green Sandpiper	*Tringa ochropus*	Y	-	4	1.2	V
Wood Sandpiper	*Tringa glareola*	Y	LC	3	1.4	V

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]	Mar 2022 Occurrence[3]	Mar 2022 Mean[4]	Records outside surveys[5]
Common Sandpiper	*Actitis hypoleucos*	Y	-	1	0.2	0
Pacific Swift	*Apus pacificus*	N	(LC)	1	0.6	0
Pied Kingfisher	*Ceryle rudis*	Y	(LC)	4	1.4	0
White-throated Kingfisher#	*Halcyon smyrnensis*	Y	Class II, (LC)	1	0.4	0
Common Kingfisher	*Alcedo atthis*	Y	-	4	1.0	0
Sand Martin	*Riparia riparia*	Y	-	1	1.2	0
Eastern Yellow Wagtail	*Motacilla tschutschensis*	Y	-	4	3.2	0
Grey Wagtail	*Motacilla cinerea*	Y	-	1	0.2	0
			No. of species recorded:	**26**		

Note:
(1) Follows HK bird list (dated 2020-03).
(2) Conservation status follows that of Fellowes *et al.* (2002) and BirdLife International listing (2017). Letters in parentheses indicate that the assessment is on the basis of restrictedness in breeding and/or roosting sites rather than in general occurrence. (Fellowes *et al*. 2002)
(3) Indicates number of surveys recorded within the reporting period.
(4) Refers to the mean number of individuals recorded in the reporting period in the WRA.
(5) Includes observations during other surveys and/or site visits.
(6) Five regular surveys and nine outside surveys were conducted
Birds tagged with '#' are Category II protected under terrestrial wildlife state protection
Birds tagged with '##" are Category I protected under terrestrial wildlife state protection
V Indicates the species is recorded outside regular surveys

Table I3: Summary of bird species recorded in the Survey Area (excluding the WRA) during the reporting month

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]
Little Grebe	*Tachybaptus ruficollis*	Y	LC
Great Cormorant	*Phalacrocorax carbo*	Y	PRC
Grey Heron	*Ardea cinerea*	Y	PRC
Great Egret	*Ardea alba*	Y	PRC, (RC)
Little Egret	*Egretta garzetta*	Y	PRC, (RC)
Eastern Cattle Egret	*Bubulcus coromandus*	Y	(LC)
Chinese Pond Heron	*Ardeola bacchus*	Y	PRC, (RC)
Black-crowned Night Heron	*Nycticorax nycticorax*	Y	(LC)
Black-faced Spoonbill##	*Platalea minor*	Y	Class I, PGC, EN
Tufted Duck	*Aythya fuligula*	Y	LC
Black Kite#	*Milvus migrans*	Y	Class II, (RC)
Eastern Buzzard#	*Buteo japonicus*	Y	Class II
White-breasted Waterhen	*Amaurornis phoenicurus*	Y	-
Common Moorhen	*Gallinula chloropus*	Y	-
Black-winged Stilt	*Himantopus himantopus*	Y	RC
Pied Avocet	*Recurvirostra avosetta*	Y	RC
Little Ringed Plover	*Charadrius dubius*	Y	(LC)
Common Redshank	*Tringa totanus*	Y	RC

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]
Common Greenshank	*Tringa nebularia*	Y	RC
Green Sandpiper	*Tringa ochropus*	Y	-
Wood Sandpiper	*Tringa glareola*	Y	LC
Common Sandpiper	*Actitis hypoleucos*	Y	-
Spotted Dove	*Spilopelia chinensis*	N	-
Eurasian Collared Dove	*Streptopelia decaocto*	N	-
Asian Koel	*Eudynamys scolopaceus*	N	-
Greater Coucal#	*Centropus sinensis*	N	Class II
Pied Kingfisher	*Ceryle rudis*	Y	(LC)
White-throated Kingfisher#	*Halcyon smyrnensis*	Y	Class II, (LC)
Common Kingfisher	*Alcedo atthis*	Y	-
Barn Swallow	*Hirundo rustica*	N	-
Eastern Yellow Wagtail	*Motacilla tschutschensis*	Y	-
Grey Wagtail	*Motacilla cinerea*	Y	-
White Wagtail	*Motacilla alba*	Y	-
Richard's Pipit	*Anthus richardi*	N	-
Olive-backed Pipit	*Anthus hodgsoni*	N	-
Red-throated Pipit	*Anthus cervinus*	N	LC
Red-whiskered Bulbul	*Pycnonotus jocosus*	N	-
Light-vented Bulbul	*Pycnonotus sinensis*	N	-
Long-tailed Shrike	*Lanius schach*	N	-
Oriental Magpie Robin	*Copsychus saularis*	N	-
Stejneger's Stonechat	*Saxicola stejnegeri*	N	-
Daurian Redstart	*Phoenicurus auroreus*	N	-
Masked Laughingthrush	*Garrulax perspicillatus*	N	-
Common Tailorbird	*Orthotomus sutorius*	N	-
Dusky Warbler	*Phylloscopus fuscatus*	N	-
Yellow-browed warbler	*Phylloscopus inornatus*	N	-
Zitting Cisticola	*Cisticola juncidis*	Y	LC
Yellow-bellied Prinia	*Prinia flaviventris*	N	-
Plain Prinia	*Prinia inornata*	N	-
Cinereous Tit	*Parus cinereus*	N	-
Swinhoe's White-eye	*Zosterops simplex*	N	-
Black-faced Bunting	*Emberiza spodocephala*	N	-
Scaly-breasted Munia	*Lonchura punctulata*	N	-
Eurasian Tree Sparrow	*Passer montanus*	N	-
Black-collared Starling	*Gracupica nigricollis*	N	-
White-shouldered Starling	*Sturnia sinensis*	Y	(LC)
Common Myna	*Acridotheres tristis*	N	-
Crested Myna	*Acridotheres cristatellus*	N	-
Azure-winged Magpie	*Cyanopica cyanus*	N	-
Large-billed Crow	*Corvus macrorhynchos*	N	-
Collared Crow	*Corvus torquatus*	Y	LC, NT
	No. of species recorded:	**61**	

Note:
(1) Follows HK bird list (dated 2020-03)

(2) Conservation status follows that of Fellowes *et al*. (2002) and BirdLife International listing (2017). Letters in parentheses indicate that the assessment is on the basis of restrictedness in breeding and/or roosting sites rather than in general occurrence. (Fellowes *et al*. 2002)
(3) Five regular surveys and three outside surveys were conducted
\# Greater Coucal is listed as vulnerable (VU) in China Red Data Book and it is protected under terrestrial wildlife state protection (category II)
Other birds tagged with '#' are Category II protected under terrestrial wildlife state protection
Birds tagged with '##" are Category I protected under terrestrial wildlife state protection

Table I4: Summary of bird species recorded in the WRA during the reporting month

Species Name(1)	Scientific Name(1)	Wetland Dependence	Conservation Status(2)
Little Grebe	*Tachybaptus ruficollis*	Y	LC
Great Cormorant	*Phalacrocorax carbo*	Y	PRC
Grey Heron	*Ardea cinerea*	Y	PRC
Great Egret	*Ardea alba*	Y	PRC, (RC)
Little Egret	*Egretta garzetta*	Y	PRC, (RC)
Chinese Pond Heron	*Ardeola bacchus*	Y	PRC, (RC)
Great Bittern	*Botaurus stellaris*	Y	RC
Black-crowned Night Heron	*Nycticorax nycticorax*	Y	(LC)
Besra#	*Accipiter virgatus*	N	Class II
Black Kite#	*Milvus migrans*	Y	Class II, (RC)
Eastern Buzzard#	*Buteo japonicus*	Y	Class II
White-breasted Waterhen	*Amaurornis phoenicurus*	Y	-
Common Moorhen	*Gallinula chloropus*	Y	-
Green Sandpiper	*Tringa ochropus*	Y	-
Wood Sandpiper	*Tringa glareola*	Y	LC
Common Sandpiper	*Actitis hypoleucos*	Y	-
Spotted Dove	*Spilopelia chinensis*	N	-
Asian Koel	*Eudynamys scolopaceus*	N	-
Greater Coucal#	*Centropus sinensis*	N	Class II
Plaintive Cuckoo	*Cacomantis merulinus*	N	-
Asian Barred Owlet#	*Glaucidium cuculoides*	N	Class II
Savanna Nightjar	*Caprimulgus affinis*	N	-
Pacific Swift	*Apus pacificus*	N	(LC)
House Swift	*Apus nipalensis*	N	-
Pied Kingfisher	*Ceryle rudis*	Y	(LC)
White-throated Kingfisher#	*Halcyon smyrnensis*	Y	Class II, (LC)
Common Kingfisher	*Alcedo atthis*	Y	-
Barn Swallow	*Hirundo rustica*	N	-
Sand Martin	*Riparia riparia*	Y	-
Eastern Yellow Wagtail	*Motacilla tschutschensis*	Y	-
Grey Wagtail	*Motacilla cinerea*	Y	-
White Wagtail	*Motacilla alba*	Y	-
Richard's Pipit	*Anthus richardi*	N	-
Olive-backed Pipit	*Anthus hodgsoni*	N	-
Red-whiskered Bulbul	*Pycnonotus jocosus*	N	-
Light-vented Bulbul	*Pycnonotus sinensis*	N	-
Long-tailed Shrike	*Lanius schach*	N	-
Oriental Magpie Robin	*Copsychus saularis*	N	-
Stejneger's Stonechat	*Saxicola stejnegeri*	N	-

Species Name[1]	Scientific Name[1]	Wetland Dependence	Conservation Status[2]
Daurian Redstart	*Phoenicurus auroreus*	N	-
Masked Laughingthrush	*Garrulax perspicillatus*	N	-
Oriental Reed Warbler	*Acrocephalus orientalis*	Y	-
Common Tailorbird	*Orthotomus sutorius*	N	-
Dusky Warbler	*Phylloscopus fuscatus*	N	-
Yellow-browed Warbler	*Phylloscopus inornatus*	N	-
Yellow-bellied Prinia	*Prinia flaviventris*	N	-
Plain Prinia	*Prinia inornata*	N	-
Chinese Penduline-Tit	*Remiz consobrinus*	Y	RC
Cinereous Tit	*Parus cinereus*	N	-
Swinhoe's White-eye	*Zosterops simplex*	N	-
Little Bunting	*Emberiza pusilla*	N	-
Black-faced Bunting	*Emberiza spodocephala*	N	-
Scaly-breasted Munia	*Lonchura punctulata*	N	-
Black-collared Starling	*Gracupica nigricollis*	N	-
Common Myna	*Acridotheres tristis*	N	-
Crested Myna	*Acridotheres cristatellus*	N	-
Collared Crow	*Corvus torquatus*	Y	LC, NT
	No. of species recorded:	**57**	

Note:
(1) Follows HK bird list (dated 2020-03)
(2) Conservation status follows that of Fellowes *et al*. (2002) and BirdLife International listing (2017). Letters in parentheses indicate that the assessment is on the basis of restrictedness in breeding and/or roosting sites rather than in general occurrence. (Fellowes *et al*. 2002)
(3) Five regular surveys and nine outside surveys were conducted
\# Greater Coucal is listed as vulnerable (VU) in China Red Data Book and it is protected under terrestrial wildlife state protection (category II)
Other birds tagged with '#' are Category II protected under terrestrial wildlife state protection
Birds tagged with '##" are Category I protected under terrestrial wildlife state protection

J. Summary of Herpetofauna, Mammal and Insect Surveys conducted

Table J1: Summary of herpetofauna monitoring in the Survey Area (excluding the WRA)

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Mean[3]	Records Outside Surveys[4]
Amphibian	**No. of species recorded:**	**3**			
Asian Common Toad	*Bufo melanostictus*	-	2	7.0	0
Paddy Frog	*Fejervarya limnocharis*	-	1	2.0	0
Brown Tree Frog	*Polypedates megacephalus*	-	1	1.0	0
Species Name	**Scientific Name**	**Conservation Status[1]**	**Mar 2022 Occurrence[2]**	**Mar 2022 Mean[3]**	**Records Outside Surveys[4]**
Reptile	**No. of species recorded:**	**1**			
Bowring's Gecko	*Hemidactylus bowringii*	-	1	8.0	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002), Chan *et al*. (2005) and Karsen *et al*. (1998).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA).
(4) Includes observations during other surveys and/or site visits.
(5) Two regular surveys and six outside surveys were conducted
V Indicates the species is recorded outside regular surveys

Table J2: Summary of herpetofauna monitoring in the WRA

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Mean[3]	Records Outside Surveys[4]
Amphibian	**No. of species recorded:**	**3**			
Asian Common Toad	*Bufo melanostictus*	-	1	3.0	0
Gunther's Frog	*Hylarana guentheri*	-	1	0.5	0
Ornate Pygmy Frog	*Microhyla fissipes*	-	1	2.5	0
Species Name	**Scientific Name**	**Conservation Status[1]**	**Mar 2022 Occurrence[2]**	**Mar 2022 Mean[3]**	**Records Outside Surveys[4]**
Reptile	**No. of species recorded:**	**3**			
Bowring's Gecko	*Hemidactylus bowringii*	-	1	3.5	0
Long-tailed Skink	*Eutropis longicaudata*	-	1	0.5	0

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Mean[3]	Records Outside Surveys[4]
Reeve's Smooth Skink	*Scincella reevesii*	-	2	2.0	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002), Chan *et al*. (2005) and Karsen *et al*. (1998).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period in the WRA.
(4) Includes observations during other surveys and/or site visits.
(5) Two regular surveys and twelve outside surveys were conducted
V Indicates the species is recorded outside regular surveys

Table J3: Summary of mammal monitoring in the Survey Area (excluding the WRA)

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Max[3]	Records Outside Surveys[4]
Mammal	**No. of species recorded:**	**2**			
Short-nosed Fruit Bat	*Cynopterus sphinx*	-	1	1	0
Japanese Pipistrelle	*Pipistrellus abramus*	-	1	2	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002) and Shek (2006).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the maximum number of individuals recorded in the reporting period (excluding the WRA).
(4) Includes observations during other surveys and/or site visits.
(5) Eight regular surveys and no outside surveys were conducted
V Indicates the species is recorded outside regular surveys

Table J4: Summary of mammal monitoring in the WRA

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Max[3]	Records Outside Surveys[4]
Mammal	**No. of species recorded:**	**2**			
Short-nosed Fruit Bat	*Cynopterus sphinx*	-	1	6	0
Japanese Pipistrelle	*Pipistrellus abramus*	-	1	6	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002) and Shek (2006).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the maximum number of individuals recorded in the reporting period in the WRA.
(4) Includes observations during other surveys and/or site visits.
(5) Eight regular surveys and six outside surveys were conducted
V Indicates the species is recorded outside regular surveys

Table J5: Summary of dragonflies (odonata) and butterfly monitoring in the Survey Area (excluding the WRA)

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Mean [3]	Records Outside Surveys[4]
Odonata	**No. of species recorded:**	**4**			
Common Bluetail	*Ischnura senegalensis*	-	1	3.0	0
Yellow Featherlegs	*Copera marginipes*	-	1	5.0	0
Asian Amberwing	*Brachythemis contaminata*	-	1	1.0	0
Wandering Glider	*Pantala flavescens*	-	1	4.0	0
Species Name	**Scientific Name**	**Conservation Status[1]**	**Mar 2022 Occurrence[2]**	**Mar 2022 Mean [3]**	**Records Outside Surveys[4]**
Butterflies	**No. of species recorded:**	**7**			
Common Sailor	*Neptis hylas hylas*	-	1	1.0	0
Dark Brand Bush Brown	*Mycalesis mineus mineus*	-	1	3.0	0
Red-base Jezebel	*Delias pasithoe pasithoe*	-	1	1.0	0
Small Cabbage White	*Pieris rapae crucivora*	-	1	41.0	0
Tailed Jay	*Graphium agamemnon agamemnon*	-	1	1.0	0
Common Mime	*Chilasa clytia clytia*	-	1	1.0	0
Great Mormon	*Papilio memnon agenor*	-	1	1.0	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002), Lo & Hui (2004), Tam *et al*. (2011) and Young & Yiu (2002).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period (excluding the WRA).
(4) Includes observations during other surveys and/or site visits.
(5) One regular survey and seven outside surveys were conducted
V Indicates the species is recorded outside regular surveys

Table J6: Summary of dragonflies (odonata) and butterfly monitoring in the WRA

Species Name	Scientific Name	Conservation Status[1]	Mar 2022 Occurrence[2]	Mar 2022 Mean [3]	Records Outside Surveys[4]
Odonata	**No. of species recorded:**	**12**			
Wandering Midget	*Agriocnemis pygmaea*	-	1	2.0	0
Orange-tailed Sprite	*Ceriagrion auranticum ryukyuanum*	-	1	5.0	0
Common Bluetail	*Ischnura senegalensis*	-	1	3.0	0
Blue Sprite	*Pseudagrion microcephalum*	LC	1	1.0	0

Species Name	Scientific Name	Conservation Status(1)	Mar 2022 Occurrence(2)	Mar 2022 Mean (3)	Records Outside Surveys(4)
Asian Amberwing	*Brachythemis contaminata*	-	1	2.0	V
Pied Percher	*Neurothemis tullia tullia*	-	1	4.0	V
Green Skimmer	*Orthetrum sabina s abina*	-	1	3.0	0
Wandering Glider	*Pantala flavescens*	-	1	1.0	0
Pied Skimmer	*Pseudothemis zonata*	-	1	1.0	0
Variegated Flutterer	*Rhyothemis variega ta arria*	-	-	-	V
Evening Skimmer	*Tholymis tillarga*	-	1	1.0	V
Dingy Dusk-darter	*Zyxomma petiolatum*	-	1	1.0	0

Species Name	Scientific Name	Conservation Status(1)	Mar 2022 Occurrence(2)	Mar 2022 Mean (3)	Records Outside Surveys(4)
Butterflies	**No. of species recorded:**	**16**			
Dark Brand Bush Brown	*Mycalesis mineus mineus*	-	1	5.0	0
Long-tailed Blue	*Lampides boeticus*	-	1	1.0	0
Pale Grass Blue	*Pseudozizeeria maha serica*	-	1	1.0	0
Lesser Grass Blue	*Zizina otis*	-	1	3.0	0
Red-base Jezebel	*Delias pasithoe pasithoe*	-	1	1.0	0
Indian Cabbage White	*Pieris canidia canidia*	-	1	1.0	0
Small Cabbage White	*Pieris rapae crucivora*	-	1	8.0	0
Lemon Emigrant	*Catopsilia pomona pomona*	-	1	1.0	0
Common Grass Yellow	*Eurema hecabe hecabe*	-	1	3.0	0
Three-spot Grass Yellow	*Eurema blanda hylama*	-	1	1.0	0
Common Mime	*Chilasa clytia clytia*	-	1	2.0	0
Red Helen	*Papilio helenus*	-	1	2.0	0
Common Mormon	*Papilio polytes polytes*	-	1	2.0	0
Paris Peacock	*Papilio paris*	-	1	2.0	0
Chinese Dart	*Potanthus confucius confucius*	-	1	1.0	0
Banana Skipper	*Erionota torus*	-	1	1.0	0

Note:
(1) Conservation status follows that of Fellowes *et al*. (2002), Lo & Hui (2004), Tam *et al*. (2011) and Young & Yiu (2002).
(2) Indicates number of surveys recorded within the reporting period.
(3) Refers to the mean number of individuals recorded in the reporting period in the WRA.
(4) Includes observations during other surveys and/or site visits.
(5) One regular survey and 13 outside surveys were conducted
V Indicates the species is recorded outside regular surveys

K. Summary of Water Quality Monitoring associated with Ecological Monitoring conducted

Table K1. Water quality at WRA during the reporting month

Cell No.	Temp. (ºC)	pH	Salinity (ppt)	Turbidity (NTU)	DO (mg/ L)	Water Level Monitoring (cm)	
						(15 Mar 2022)	(29 Mar 2022)
1	26.9	7.1	0.3	5.3	5.6	170	175
2	27.0	7.2	0.3	8.2	6.0	165	165
3	27.1	7.4	0.3	5.1	6.3	200	210
4	26.8	7.3	0.3	5.2	6.5	190	200
Action Level	-	<6.5 or >8.0	>2	-	<2	<150 or >250	
Limit Level	-	<6.0 or >8.5	>5	-	<1	-	

Notes:
1. Values highlighted in **bold** indicate that action level is reached; whereas values in **bold and underlined** indicate that limit level is reached.
2. Water level monitoring was conducted on 15 and 29 March 2022.
3. Monitoring of all other parameters was conducted on 22 March 2022.

L. Environmental Mitigation Measures - Implementation Status

Air Quality – Recommended Mitigation Measures

Air Quality Mitigation Measures during construction	Implementation Status
• access roads should be sprayed with water or dust suppression chemical to maintain the entire road surface wet or paved;	✓
• every stock of more than 20 bags of cement or dry PFA should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;	N/A
• de-bagging, batching or mixing process should be carried out in sheltered areas during the use of bagged cement;	N/A
• use of effective dust screens, sheeting or netting to be provided to enclose dry scaffolding which may be provided from the ground floor level of the building or if a canopy is provided at the first-floor level, from the first floor level, up to the highest level (maximum four floors for this Project) of the scaffolding where scaffolding is erected around the perimeter of a building under construction;	N/A
• dump trucks for material transport should be totally enclosed using impervious sheeting;	✓
• any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading;	✓
• dusty materials remaining after a stockpile is removed should be wetted with water;	✓
• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with e.g. concrete, bituminous materials or hardcore or similar;	✓
• the portion of road leading only to a construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;	✓
• stockpile of dusty materials to be either covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides; or sprayed with water so as to maintain the entire surface wet;	✓
• all dusty materials to be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty material wet;	✓
• vehicle speed to be limited to 10 kph except on completed access roads;	✓
• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites;	✓
• the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; and	✓
• the working area of excavation should be sprayed with water immediately before, during and immediately after (as necessary) the operations so as to maintain the entire surface wet.	✓
Odour mitigation measures	
• all malodorous excavated material should be placed as far as possible from any ASRs;	N/A
• the stockpiled malodorous material should be removed from site as soon as possible; and	N/A
• the stockpiled malodorous material should be covered entirely by plastic tarpaulin sheets.	N/A

Noise – Recommended Mitigation Measures

Noise Mitigation Measures during construction	Implementation Status
• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works;	✓
• machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;	✓
• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs;	✓
• silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction period;	✓
• mobile plant should be sited as far away from NSRs as possible;	✓
• material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities; and	✓
• air compressor and hand-held breaker should be fitted with valid noise emission labels during operation; and	N/A
• The Contractor shall at all times comply with all current statutory environmental legislation.	✓
Selection of quieter plant and working methods The Contractor shall obtain particular models of plant that are quieter than standards given in GW-TM. The list of assumed quieter plants can be found in the Table 4–14 of the EIA report. The Contractor shall select from the available models achieving the assumed sound levels while making reference to the GW-TM, BS 5228-1:2009+A1:2014 and BS 5228-2:2009+A1:2014	✓
Use of Noise Barriers Noise barriers are proposed along the site boundary to block the direct line of sight from the most affected NSRs to the major noise contribution construction phases. The height of the noise barriers ranged from 9-10m. The noise barriers shall be built before the commencement of construction works in order to ensure protection to nearby NSRs. The noise barrier should have a surface density of at least 10kg/m^2 or material providing equivalent transmission loss. The noise barriers and hoardings should have no gaps and openings to avoid noise leakage.	P

Water Quality – Recommended Mitigation Measures

Water Quality Mitigation Measures during construction	Implementation Status
• The site should be confined to avoid silt runoff to the site.	✓
• No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site.	✓
• Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.	✓
• Stockpiles to be covered by tarpaulin to avoid spreading of materials during rainstorms;	N/A
• Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;	✓
• Chemical waste containers shall be labelled with appropriate warning signs in English and Chinese to avoid accidents. there shall also be clear instructions showing what action to take in the event of an accidental;	✓
• Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area;	✓
• Any construction plant which causes pollution to the water system due to leakage of oil or fuel shall be removed off-site immediately;	N/A
• Spillage or leakage of chemical waste to be controlled by using suitable absorbent materials;	N/A
• Chemicals will always be stored on drip trays or in bunded areas where the volume is 110% of the stored volume;	P

Water Quality Mitigation Measures during construction	Implementation Status
• Regular clearance of domestic waste generated in the temporary sanitary facilities to avoid wastewater spillage.	✓
• Temporary sanitary facilities to be provided for on-site workers during construction.	✓
• Temporary drainage channel and associated facilities will be provided to collect the surface runoff generated within the Project Area during the construction phase.	✓
• Sandbags or silt traps will need to be placed to avoid silt runoff to the drainage channel draining the water in the northern ditch. Draining of the ditches should avoid rainy weather.	✓
• Excavated soil which needs to be temporarily stockpiled should be stored in a specially designated area and provided with a tarpaulin cover to avoid runoff into the drainage channels.	✓

Waste Management – Recommended Mitigation Measures

Waste Management Mitigation Measures during construction	Implementation Status
Site Clearance Waste	✓
• The major construction works of Wo Shang Wai is in the development of residential buildings and other associated facilities (club house, tennis courts, etc.). The amount of site clearance works will be limited with the exception of the excavated materials. The thin layer of vegetation removed can be stored and reused for landscaping.	
Excavated Materials	✓
The intention is to maximize the reuse of the excavated materials on-site as fill materials.	
Imported Filling Material	✓
The excavated/imported filling material may have to be temporarily stockpiled on-site for the construction of road embankment and foundation of viaduct substructure. Control measures should be taken at the stockpiling area to prevent the generation of dust and pollution of stormwater channels. However, to eliminate the risk of blocking drains in the wet season, it is recommended that stockpiling of excavated materials at during wet season should be avoided as far as practicable.	
Construction and Demolition Materials	✓
Careful design, planning and good site management can minimise over-ordering and generation of waste materials such as concrete, mortars and cement grouts. The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork of plastic facing should be considered to increase the potential for reuse.	
The Contractor should reuse any C&D material on-site. C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal.	✓
Chemical Waste	N/A
For those processes which generate chemical waste, it may be possible to find alternatives which generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste.	
Containers used for the storage of chemical wastes should:	
• be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed:	✓
• have a capacity of less than 450 litres unless the specification has been approved by the EPD; and	✓
• display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations,	✓
The storage area for chemical wastes should:	
• be clearly labelled and used solely for the storage of chemical waste;	✓
• be enclosed on at least 3 sides;	✓

Waste Management Mitigation Measures during construction	Implementation Status
• have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area whichever is the greatest;	✓
• have adequate ventilation;	✓
• be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and	✓
• be arranged so that incompatible materials are adequately separated.	✓
Disposal of chemical waste should:	
• be via a licensed waste collector; and	N/A
• be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers, or	N/A
• to be a re-user of the waste, under approval from the EPD.	N/A
General Refuse Should be stored in enclosed bins or compaction units separate from C&D and chemical wastes. The Contractor should employ a reputable waste collector to remove general refuse from the site, separate from C&D and chemical wastes, on a regular basis to minimise odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.	P
Disposal of Excavated Sediment at Sea	
The requirements and procedures for excavated sediment disposal are specified under the ETWB TC(W) No. 34/2002 and PNAP 252 (ADV-21). The management of the excavation, use and disposal of sediment is monitored by Fill Management Committee, whilst the licensing of marine dumping is the responsibility of the Director of Environmental Protection (DEP).	N/A
The excavated sediment would be loaded onto barges or other appropriate vessel and transported to the designated marine disposal site. Category L sediment and Category M sediment passing the biological test would be suitable for disposal at a gazetted open sea disposal ground. Category M sediment failing the biological test and Category H sediment passing the biological test would require confined marine disposal.	N/A
During transportation and disposal of the dredged sediment, the following measures should be taken to minimize potential impacts on water quality: -	N/A
• Bottom opening transport vessels should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of vessels before the vessel is moved.	N/A
• Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP.	N/A

Ecology – Recommended Mitigation Measures

Ecology Mitigation Measures during construction	Implementation Status
Clear Definition of Site Limit	
Clear definition of the site limit should be provided in order to minimize and confine the disturbance during the construction period, especially the northern limit of the Site which is adjacent to fishponds within the Conservation Area (CA) zone and are considered to be ecological sensitive receivers.	✓
During wetland construction stage the WRA boundary will be delineated using a temporary hoarding in order to reduce disturbance to off-site habitats and wildlife. During the establishment phase this hoarding will be replaced with a 1 m high chain-link fence in order to reduce disturbance to the WRA through access by humans and dogs, and a hoarding will be established around the residential construction site.	N/A (WRA construction completed)

Ecology Mitigation Measures during construction	Implementation Status
Dust and Noise Suppression and Avoidance of Water Pollution	
Good site practices of dust and noise suppression should be strictly implemented to ensure that disturbance is minimized to acceptable levels. Mitigation measures for the off-site disturbance impacts on the fishponds in the CA include hoarding at the northern site boundary during construction of the WRA to reduce noise and dust impacts to the adjacent habitats. Through the use of quieter plant and temporary/movable noise barriers, the noise level would be reduced significantly to an acceptable level. Hoarding at the northern boundary should be replaced with a 1 m high chain-link fence following construction and the WRA will then act as a buffer between the existing wetland areas and the residential part of the site until construction is completed. Hoarding will be retained between the WRA and ongoing construction work to avoid visual disturbance and reduce noise and dust emissions. Pollution of watercourses and sedimentary runoff will be minimized by good site practice, especially the containment of water and sediment within the site for removal. These standard noise and air and water quality site practices are considered to be effective measures for minimizing the disturbance impact during the construction period.	✓
Planning of Construction Schedule	
The construction of the proposed project should be scheduled in phases. Because mitigation is preferably carried out in advance of the main works rather than after the completion of works, the construction of the WRA will commence at the start of the project. Construction work within the WRA is scheduled to take place in a single wet season, followed by 1.5 years of wetland establishment. During the wetland establishment period no noisy work will be undertaken within the WRA to minimize the disturbance to off-site habitats and wildlife.	N/A (WRA construction completed)
Reusing Onsite Materials	
Soil and plants on-site should be reused (e.g. used as fill material) as far as practical. Stockpiles of these reusable materials should be stored in an appropriate area on-site. In particular, the re-use of the wetland soils and topsoil should be considered.	✓
Construction of the Wetland Restoration Area The WRA will be operational within 2.5 yrs from the commencement of construction (1 year for site formation and 1.5 years for establishment) and will compensate for the predicted ecological impacts of the proposed development.	✓

Landscape and Visual – Recommended Mitigation Measures

Landscape and Visual Mitigation Measures during construction	Implementation Status
CM1 - The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape.	✓
CM2 - Screening of construction works by hoarding / noise barriers.	✓ (see **Appendix M** Photo 1 & 3 *)
CM3 - Reduction of construction period to practical minimum.	✓
CM4 - Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where the soil material meets acceptable criteria and where practical. The Contract Specification shall include storage and reuse of topsoil as appropriate.	✓
CM5 - Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone).	✓
CM6 - Advance screen planting of noise barriers	✓ (see **Appendix M** Photo 3 *)
CM7 - Control night-time lighting and glare by hooding all lights.	N/A
CM8 - Ensure no run-off into streams adjacent to the Project Area.	✓
CM9 - Protection of existing trees on boundary of site shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained	✓

Landscape and Visual Mitigation Measures during construction	Implementation Status
trees, including trees in contractor's works areas. (Tree protection measures will be detailed at S16 and Tree Removal Application stage).	
CM10 - Trees unavoidably affected by the works shall be transplanted where practical. Trees should be transplanted straight to their destinations and not held in a nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.	✓

Legend:
✓ Implemented
× Not implemented
P Partially implemented
N/A Not applicable
* Representative photos showing the implementation of mitigation measures are presented in **Appendix M**

M. Landscape and Visual Audit Photos

Photo 1: The Construction works have been screened by hoarding / noise barriers. (CM2)	Photo 2: The wetland areas are being established, and the ponds are being seasonally filled with rainwater. (OM4)
Photo 3: Advance screen planting of noise barrier has been undertaken (CM6, OM2)	
